
MLTX-02-005 - Playground Initiative for Eastern Region (Arar-Hasa osis -Dammam)

Remaining work
D.D 26-10-2026

Activity ID	Activity Name	Original Duration	Schedule % Complete	Performance % Complete	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Variance - BL Project
MLTX-02-005 Playground Initiative for Eastern Region (Arar - Hasa Oa		190	10.03%	7.57%	04-May-26	02-Jan-27	01-Jun-26 A	14-Mar-27	1,938,218.01	1,462,761.11	19,322,761.75	-57
KEY MILESTONES		62	0%	0%	17-Dec-26	02-Jan-27	27-Dec-26	14-Mar-27	0.00	0.00	0.00	-57
GENERAL MILESTONES		0	0%	0%	02-Jan-27	02-Jan-27	14-Mar-27	14-Mar-27	0.00	0.00	0.00	-57
MLTX-02-005-MS-1030	Project Completion	0	0%	0%		02-Jan-27		14-Mar-27	0.00	0.00	0.00	-57
CONTRACTUAL MILESTONE		61	0%	0%	17-Dec-26	02-Jan-27	27-Dec-26	09-Mar-27	0.00	0.00	0.00	-56
MLTX-02-005-MS-1070	Completion of Testing & Commissioning	0	0%	0%		02-Jan-27		09-Mar-27	0.00	0.00	0.00	-56
MLTX-02-005-MS-1100	Completion of Engineering	0	0%	0%		17-Dec-26		27-Dec-26	0.00	0.00	0.00	-8
MLTX-02-005-MS-1130	Completion of Toilet Building	0	0%	0%		31-Dec-26		01-Mar-27	0.00	0.00	0.00	-50
MLTX-02-005-MS-1140	Completion of Playground Area	0	0%	0%		31-Dec-26		01-Mar-27	0.00	0.00	0.00	-50
MLTX-02-005-MS-1150	Completion of Natural Landscape Works	0	0%	0%		31-Dec-26		01-Mar-27	0.00	0.00	0.00	-50
MLTX-02-005-MS-1160	Completion of Arar Works	0	0%	0%		31-Dec-26		01-Mar-27	0.00	0.00	0.00	-50
MLTX-02-005-MS-1170	Completion of Hasa Oasis Works	0	0%	0%		31-Dec-26		01-Mar-27	0.00	0.00	0.00	-50
MLTX-02-005-MS-1180	Completion of Dammam Works	0	0%	0%		31-Dec-26		28-Feb-27	0.00	0.00	0.00	-49
ARAR		144	10.31%	4.74%	27-Jun-26	02-Jan-27	11-Jun-26 A	01-Mar-27	706,991.96	325,136.04	6,855,947.95	-49
ENGINEERING		53	0%	0%	19-Sep-26	08-Dec-26	27-Oct-26	27-Dec-26	0.00	0.00	0.00	-16
SHOP DRAWINGS		53	0%	0%	19-Sep-26	08-Dec-26	27-Oct-26	27-Dec-26	0.00	0.00	0.00	-16
SHOP DRAWINGS SUBMISSION		27	0%	0%	19-Sep-26	20-Oct-26	27-Oct-26	26-Nov-26	0.00	0.00	0.00	-32
SHOP DRAWINGS SUBMITTALS FOR PLAYGROUND WORKS		27	0%	0%	19-Sep-26	20-Oct-26	27-Oct-26	26-Nov-26	0.00	0.00	0.00	-32
ELECTRICAL WORKS		27	0%	0%	19-Sep-26	20-Oct-26	27-Oct-26	26-Nov-26	0.00	0.00	0.00	-32
MLTX-02-005-EI	Shop DWG Submittal for Power Layout	27	100%	0%	19-Sep-26	20-Oct-26	27-Oct-26	26-Nov-26	0.00	0.00	0.00	-32
SHOP DRAWINGS APPROVALS		26	0%	0%	09-Nov-26	08-Dec-26	28-Nov-26	27-Dec-26	0.00	0.00	0.00	-16
SHOP DRAWINGS APPROVAL FOR PLAYGROUND WORKS		26	0%	0%	09-Nov-26	08-Dec-26	28-Nov-26	27-Dec-26	0.00	0.00	0.00	-16
ELECTRICAL WORKS		26	0%	0%	09-Nov-26	08-Dec-26	28-Nov-26	27-Dec-26	0.00	0.00	0.00	-16
MLTX-02-005-EI	Shop DWG Approval for Power Layout	13	0%	0%	09-Nov-26	23-Nov-26	28-Nov-26	12-Dec-26	0.00	0.00	0.00	-16
MLTX-02-005-EI	Shop DWG Approval for Power Installation Details	13	0%	0%	24-Nov-26	08-Dec-26	13-Dec-26	27-Dec-26	0.00	0.00	0.00	-16
PROCUREMENT		87	0%	0%	27-Jun-26	15-Dec-26	27-Oct-26	04-Feb-27	0.00	0.00	0.00	-44
SHORT LEAD ITEM		87	0%	0%	27-Jun-26	15-Dec-26	27-Oct-26	04-Feb-27	0.00	0.00	0.00	-44
TOILET/SERVICE WORKS		69	0%	0%	27-Jun-26	28-Nov-26	27-Oct-26	14-Jan-27	0.00	0.00	0.00	-41
LIGHTING FIXTURES		40	0%	0%	27-Jun-26	11-Aug-26	27-Oct-26	12-Dec-26	0.00	0.00	0.00	-104
MLTX-02-005-PR-E	Material Delivery for Lighting Fixtures	40	100%	0%	27-Jun-26	11-Aug-26	27-Oct-26	12-Dec-26	0.00	0.00	0.00	-104
SWITCHES/SOCKETS		27	0%	0%	28-Oct-26	28-Nov-26	27-Oct-26	26-Nov-26	0.00	0.00	0.00	1
MLTX-02-005-PR-E	Material Delivery for Switches/Sockets	27	0%	0%	28-Oct-26	28-Nov-26	27-Oct-26	26-Nov-26	0.00	0.00	0.00	1
DISTRIBUTION PANNELS		15	0%	0%	04-Oct-26	20-Oct-26	30-Nov-26	16-Dec-26	0.00	0.00	0.00	-49
MLTX-02-005-PR-E	Material Delivery for Distribution Panels	15	100%	0%	04-Oct-26	20-Oct-26	30-Nov-26	16-Dec-26	0.00	0.00	0.00	-49
FURNITURES		69	0%	0%	30-Aug-26	19-Nov-26	27-Oct-26	14-Jan-27	0.00	0.00	0.00	-48
MLTX-02-005-PR-E	PO for Furnitures	29	100%	0%	30-Aug-26	03-Oct-26	27-Oct-26	29-Nov-26	0.00	0.00	0.00	-49
MLTX-02-005-PR-E	Material Delivery for Furnitures	40	47.5%	0%	05-Oct-26	19-Nov-26	30-Nov-26	14-Jan-27	0.00	0.00	0.00	-48
PLAYGROUND WORKS		87	0%	0%	15-Jul-26	15-Dec-26	27-Oct-26	04-Feb-27	0.00	0.00	0.00	-44
PVC MEMBRANE		21	0%	0%	29-Sep-26	22-Oct-26	14-Nov-26	07-Dec-26	0.00	0.00	0.00	-39
MLTX-02-005-PR-E	Material Delivery for PVC Membrane	21	100%	0%	29-Sep-26	22-Oct-26	14-Nov-26	07-Dec-26	0.00	0.00	0.00	-39
ARTIFICIAL TURF		12	0%	0%	26-Oct-26	08-Nov-26	02-Jan-27	14-Jan-27	0.00	0.00	0.00	-58
MLTX-02-005-PR-E	Material Delivery for Artificial TURF	12	8.33%	0%	26-Oct-26	08-Nov-26	02-Jan-27	14-Jan-27	0.00	0.00	0.00	-58
RUBBER GRANULES		32	0%	0%	10-Oct-26	15-Nov-26	14-Nov-26	20-Dec-26	0.00	0.00	0.00	-30
MLTX-02-005-PR-E	Material Delivery for Rubber Granules	32	46.88%	0%	10-Oct-26	15-Nov-26	14-Nov-26	20-Dec-26	0.00	0.00	0.00	-30
PADEL GLASS		18	0%	0%	16-Nov-26	06-Dec-26	16-Jan-27	04-Feb-27	0.00	0.00	0.00	-52
MLTX-02-005-PR-E	Material Delivery for Padel Glass	18	0%	0%	16-Nov-26	06-Dec-26	16-Jan-27	04-Feb-27	0.00	0.00	0.00	-52
PADEL WIRE MESH/STEEL SETS		15	0%	0%	31-Aug-26	16-Sep-26	27-Oct-26	12-Nov-26	0.00	0.00	0.00	-48
MLTX-02-005-PR-E	Material Delivery for Wire Mesh/Steel Sets	15	100%	0%	31-Aug-26	16-Sep-26	27-Oct-26	12-Nov-26	0.00	0.00	0.00	-48
BITUMINOUS BASE & WEARING COURSE		27	0%	0%	29-Sep-26	29-Oct-26	14-Nov-26	14-Dec-26	0.00	0.00	0.00	-39
MLTX-02-005-PR-S	Material Delivery for the Site	27	88.89%	0%	29-Sep-26	29-Oct-26	14-Nov-26	14-Dec-26	0.00	0.00	0.00	-39
INTERLOCKING PAVING		17	0%	0%	11-Nov-26	30-Nov-26	24-Dec-26	12-Jan-27	0.00	0.00	0.00	-37
MLTX-02-005-PR-S	Material Delivery for Interlocking Block Pavers	17	0%	0%	11-Nov-26	30-Nov-26	24-Dec-26	12-Jan-27	0.00	0.00	0.00	-37
MARKING PAINT		57	0%	0%	10-Sep-26	19-Oct-26	27-Oct-26	31-Dec-26	0.00	0.00	0.00	-63
MLTX-02-005-PR-S	PO for Marking Paint	15	100%	0%	10-Sep-26	28-Sep-26	27-Oct-26	12-Nov-26	0.00	0.00	0.00	-39
MLTX-02-005-PR-S	Material Delivery for Marking Paint	17	100%	0%	30-Sep-26	19-Oct-26	13-Dec-26	31-Dec-26	0.00	0.00	0.00	-63
AIR DIFUSSERS/GRILLS		20	0%	0%	29-Sep-26	21-Oct-26	14-Nov-26	06-Dec-26	0.00	0.00	0.00	-39
MLTX-02-005-PR-S	PO for Air Difussers/Grills	5	100%	0%	29-Sep-26	04-Oct-26	14-Nov-26	18-Nov-26	0.00	0.00	0.00	-39
MLTX-02-005-PR-S	Material Delivery for Air Difussers/Grills	15	100%	0%	05-Oct-26	21-Oct-26	19-Nov-26	06-Dec-26	0.00	0.00	0.00	-39
DISTRIBUTION BOARDS		20	0%	0%	29-Sep-26	21-Oct-26	14-Nov-26	06-Dec-26	0.00	0.00	0.00	-39
MLTX-02-005-PR-S	PO for Distribution Boards	5	100%	0%	29-Sep-26	04-Oct-26	14-Nov-26	18-Nov-26	0.00	0.00	0.00	-39
MLTX-02-005-PR-S	Material Delivery for Distribution Boards	15	100%	0%	05-Oct-26	21-Oct-26	19-Nov-26	06-Dec-26	0.00	0.00	0.00	-39
POWER CABLES		60	0%	0%	05-Oct-26	15-Dec-26	19-Nov-26	27-Jan-27	0.00	0.00	0.00	-37
MLTX-02-005-PR-S	PO for Power Cables	5	100%	0%	05-Oct-26	10-Oct-26	19-Nov-26	24-Nov-26	0.00	0.00	0.00	-39

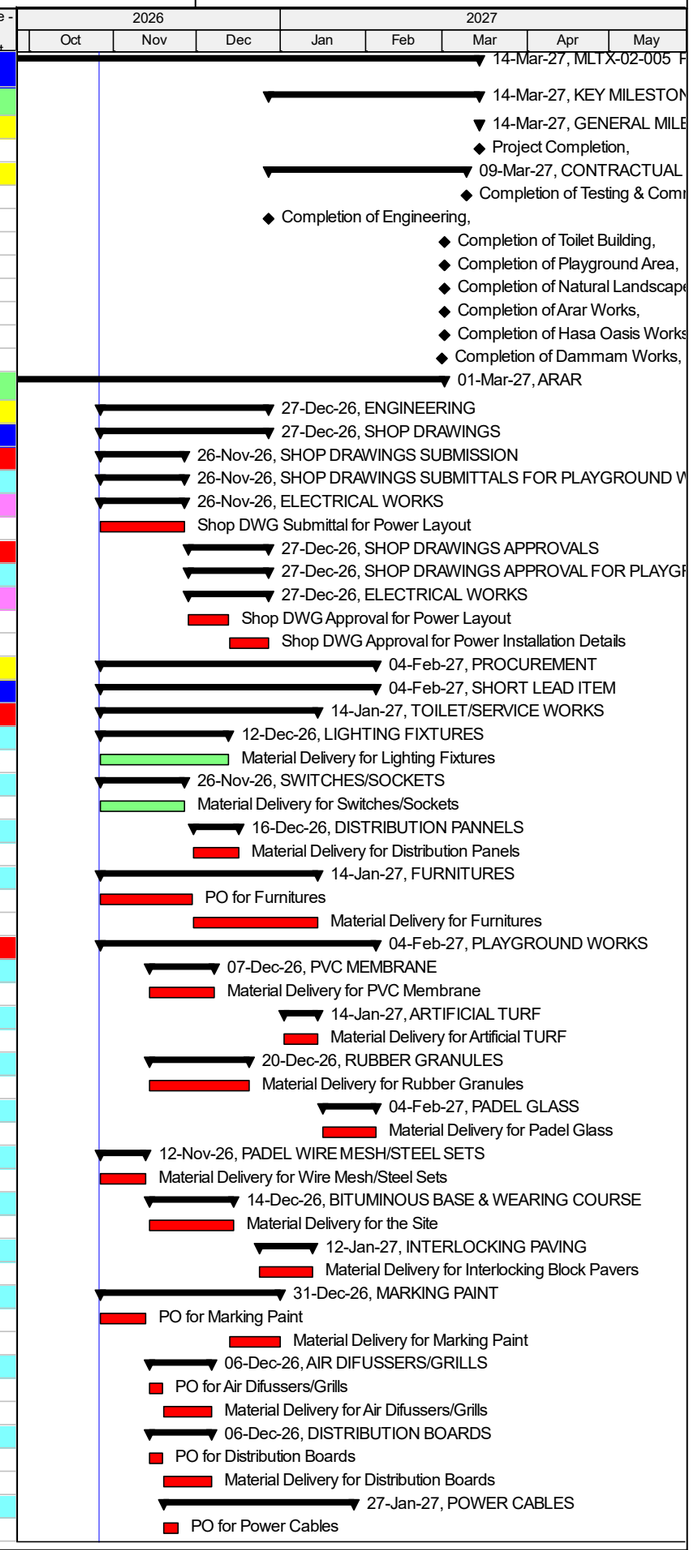

Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary

TASK filter: Remaining works.

© Oracle Corporation

MLTX-02-005 - Playground Initiative for Eastern Region (Arar-Hasa osis -Dammam)


Remaining work
D.D 26-10-2026

PROFAST شركة برو فاست المحدودة

egis

MODON مدن

Activity ID	Activity Name	Original Duration	Schedule % Complete	Performance % Complete	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Variance - BL Project
MLTX-02-005-PR-9	Material Delivery for Power Cables	30	0%	0%	11-Nov-26	15-Dec-26	24-Dec-26	27-Jan-27	0.00	0.00	0.00	-37
LIGHT FIXTURES		10	0%	0%	11-Oct-26	21-Oct-26	25-Nov-26	06-Dec-26	0.00	0.00	0.00	-39
MLTX-02-005-PR-9	Material Delivery for Light Fixtures	10	100%	0%	11-Oct-26	21-Oct-26	25-Nov-26	06-Dec-26	0.00	0.00	0.00	-39
CCTV MATERIALS		50	0%	0%	26-Sep-26	10-Nov-26	27-Oct-26	23-Dec-26	0.00	0.00	0.00	-37
MLTX-02-005-PR-9	PO for CCTV	25	100%	0%	26-Sep-26	24-Oct-26	27-Oct-26	24-Nov-26	0.00	0.00	0.00	-27
MLTX-02-005-PR-9	Material Delivery for CCTV	15	13.33%	0%	25-Oct-26	10-Nov-26	07-Dec-26	23-Dec-26	0.00	0.00	0.00	-37
POWER OUTLETS/SWITCHES		30	0%	0%	15-Jul-26	18-Aug-26	27-Oct-26	30-Nov-26	0.00	0.00	0.00	-88
MLTX-02-005-PR-9	Material Delivery for Power Outlets/Switches	30	100%	0%	15-Jul-26	18-Aug-26	27-Oct-26	30-Nov-26	0.00	0.00	0.00	-88
LANDSCAPE WORKS		87	0%	0%	15-Jul-26	23-Nov-26	27-Oct-26	04-Feb-27	0.00	0.00	0.00	-63
PAVEMENT MARKING		87	0%	0%	15-Jul-26	23-Nov-26	27-Oct-26	04-Feb-27	0.00	0.00	0.00	-63
MLTX-02-005-PR-9	PO for Pavement Markings	5	100%	0%	15-Jul-26	20-Jul-26	27-Oct-26	01-Nov-26	0.00	0.00	0.00	-88
MLTX-02-005-PR-9	Material Delivery for Pavement Markings	30	20%	0%	20-Oct-26	23-Nov-26	02-Jan-27	04-Feb-27	0.00	0.00	0.00	-63
TRAFFIC SIGNS		30	0%	0%	13-Aug-26	16-Sep-26	27-Oct-26	30-Nov-26	0.00	0.00	0.00	-63
MLTX-02-005-PR-9	Material Delivery for Traffic Signs	30	100%	0%	13-Aug-26	16-Sep-26	27-Oct-26	30-Nov-26	0.00	0.00	0.00	-63
AGRICULTURE SOIL		22	0%	0%	18-Aug-26	12-Sep-26	27-Oct-26	21-Nov-26	0.00	0.00	0.00	-59
MLTX-02-005-PR-9	Material Delivery for Agriculture Soil	22	100%	0%	18-Aug-26	12-Sep-26	27-Oct-26	21-Nov-26	0.00	0.00	0.00	-59
TRACK SURFACE		10	0%	0%	17-Sep-26	29-Sep-26	01-Dec-26	12-Dec-26	0.00	0.00	0.00	-63
MLTX-02-005-PR-9	Material Delivery for Track Surface	10	100%	0%	17-Sep-26	29-Sep-26	01-Dec-26	12-Dec-26	0.00	0.00	0.00	-63
GRASS/TREES		25	0%	0%	20-Oct-26	17-Nov-26	27-Oct-26	24-Nov-26	0.00	0.00	0.00	-6
MLTX-02-005-PR-9	Material Delivery for Grass/Trees	25	24%	0%	20-Oct-26	17-Nov-26	27-Oct-26	24-Nov-26	0.00	0.00	0.00	-6
LONG LEAD ITEM		65	0%	0%	27-Sep-26	10-Dec-26	27-Oct-26	10-Jan-27	0.00	0.00	0.00	-26
PLAYGROUND WORKS		65	0%	0%	27-Sep-26	10-Dec-26	27-Oct-26	10-Jan-27	0.00	0.00	0.00	-26
STEEL TENSION CABLES		27	0%	0%	27-Sep-26	27-Oct-26	27-Oct-26	26-Nov-26	0.00	0.00	0.00	-26
MLTX-02-005-PR-8	Material Delivery for Steel Tension Cables	15	100%	0%	27-Sep-26	13-Oct-26	27-Oct-26	12-Nov-26	0.00	0.00	0.00	-26
MLTX-02-005-PR-9	Staging time	12	91.67%	0%	14-Oct-26	27-Oct-26	14-Nov-26	26-Nov-26	0.00	0.00	0.00	-26
EMERGENCY DOORS		65	0%	0%	26-Oct-26	05-Dec-26	27-Oct-26	10-Jan-27	0.00	0.00	0.00	-31
MLTX-02-005-PR-8	Material Delivery for Emergency Doors	20	5%	0%	26-Oct-26	17-Nov-26	27-Oct-26	18-Nov-26	0.00	0.00	0.00	-1
MLTX-02-005-PR-9	Staging time	15	0%	0%	18-Nov-26	05-Dec-26	24-Dec-26	10-Jan-27	0.00	0.00	0.00	-31
PRESSURE UNITS		30	0%	0%	26-Oct-26	29-Nov-26	27-Oct-26	30-Nov-26	0.00	0.00	0.00	-1
MLTX-02-005-PR-8	Material Delivery for Pressure Units	25	4%	0%	26-Oct-26	23-Nov-26	27-Oct-26	24-Nov-26	0.00	0.00	0.00	-1
MLTX-02-005-PR-9	Staging time	5	0%	0%	24-Nov-26	29-Nov-26	25-Nov-26	30-Nov-26	0.00	0.00	0.00	-1
AIR LOCK DOORS		50	0%	0%	14-Oct-26	10-Dec-26	27-Oct-26	23-Dec-26	0.00	0.00	0.00	-11
MLTX-02-005-PR-8	Material Fabrication for Lock Doors	20	55%	0%	14-Oct-26	05-Nov-26	27-Oct-26	18-Nov-26	0.00	0.00	0.00	-11
MLTX-02-005-PR-8	Material Delivery for Lock Doors	25	0%	0%	07-Nov-26	05-Dec-26	19-Nov-26	17-Dec-26	0.00	0.00	0.00	-11
MLTX-02-005-PR-9	Staging time	5	0%	0%	06-Dec-26	10-Dec-26	19-Dec-26	23-Dec-26	0.00	0.00	0.00	-11
CONSTRUCTION PHASE		144	10.31%	4.74%	13-Sep-26	30-Dec-26	11-Jun-26 A	01-Mar-27	706,991.96	325,136.04	6,855,947.95	-51
SITE WORKS		126	8.39%	4.3%	17-Sep-26	30-Dec-26	11-Jun-26 A	01-Mar-27	530,330.98	271,853.15	6,319,424.95	-51
LANDSCAPE WORKS		126	8.39%	4.3%	17-Sep-26	30-Dec-26	11-Jun-26 A	01-Mar-27	530,330.98	271,853.15	6,319,424.95	-51
PLAYGROUND AREA		107	4.69%	0%	01-Oct-26	27-Dec-26	27-Oct-26	01-Mar-27	32,211.36	0.00	686,514.50	-54
FOOTBALL PLAYGROUND		34	0%	0%	17-Nov-26	13-Dec-26	13-Dec-26	20-Jan-27	0.00	0.00	205,952.49	-33
MLTX-02-005-CI	Finishing Asphalt & Concrete Surface (Football Playground)	15	0%	0%	17-Nov-26	03-Dec-26	13-Dec-26	29-Dec-26	0.00	0.00	158,424.99	-22
MLTX-02-005-CI	Install Sport Equipments - Goal / Nets - (Football Playground)	5	0%	0%	08-Dec-26	13-Dec-26	16-Jan-27	20-Jan-27	0.00	0.00	31,685.00	-33
MLTX-02-005-CI	Surface Marking and Painting Finishing Work (Football	5	0%	0%	08-Dec-26	13-Dec-26	16-Jan-27	20-Jan-27	0.00	0.00	15,842.50	-33
PADEL PLAYGROUND		5	0%	0%	14-Dec-26	19-Dec-26	16-Jan-27	20-Jan-27	0.00	0.00	70,195.20	-28
MLTX-02-005-CI	Install Sport Equipments - Goal / Nets - (Padel Playground)	5	0%	0%	14-Dec-26	19-Dec-26	16-Jan-27	20-Jan-27	0.00	0.00	58,496.00	-28
MLTX-02-005-CI	Surface Marking and Painting Finishing Work (Padel	5	0%	0%	14-Dec-26	19-Dec-26	16-Jan-27	20-Jan-27	0.00	0.00	11,699.20	-28
BASKETBALL PLAYGROUND		9	0%	0%	14-Dec-26	23-Dec-26	16-Jan-27	25-Jan-27	0.00	0.00	96,956.10	-28
MLTX-02-005-CI	Install Sport Equipments - Goal / Nets - (Basketball	5	0%	0%	14-Dec-26	19-Dec-26	16-Jan-27	20-Jan-27	0.00	0.00	80,796.75	-28
MLTX-02-005-CI	Surface Marking and Painting Finishing Work (Basketball	4	0%	0%	20-Dec-26	23-Dec-26	21-Jan-27	25-Jan-27	0.00	0.00	16,159.35	-28
PADEL FENCE		40	24.24%	0%	01-Oct-26	16-Nov-26	27-Oct-26	12-Dec-26	32,211.36	0.00	132,890.04	-22
MLTX-02-005-CI	Tempered Glass Fenc Installation and Fixation	20	100%	0%	01-Oct-26	24-Oct-26	27-Oct-26	18-Nov-26	30,677.48	0.00	30,677.48	-22
MLTX-02-005-CI	Chain Link Fence Installation and Fixation	20	10%	0%	25-Oct-26	16-Nov-26	19-Nov-26	12-Dec-26	1,533.87	0.00	15,338.75	-22
MLTX-02-005-CI	Install of Fence Gates	12	0%	0%	03-Nov-26	16-Nov-26	29-Nov-26	12-Dec-26	0.00	0.00	86,873.81	-22
CURBSTOEN/INTERLOCK		20	0%	0%	05-Dec-26	27-Dec-26	06-Feb-27	01-Mar-27	0.00	0.00	180,520.67	-54
MLTX-02-005-CI	Interlock Installation (Grey Scale) for LandScape (Including	20	0%	0%	05-Dec-26	27-Dec-26	06-Feb-27	01-Mar-27	0.00	0.00	180,520.67	-54
AIR DOME		44	0%	0%	15-Nov-26	21-Dec-26	23-Dec-26	11-Feb-27	0.00	0.00	4,306,367.09	-45
CIVIL WORKS		20	0%	0%	15-Nov-26	07-Dec-26	23-Dec-26	14-Jan-27	0.00	0.00	1,391,301.90	-33
MLTX-02-005-CI	Install of Membrane Covering System (Air Dome)	20	0%	0%	15-Nov-26	07-Dec-26	23-Dec-26	14-Jan-27	0.00	0.00	942,830.33	-33
MLTX-02-005-CI	Thermal Insulation Works (Air Dome)	20	0%	0%	15-Nov-26	07-Dec-26	23-Dec-26	14-Jan-27	0.00	0.00	448,471.57	-33
MECHANICAL WORKS		10	0%	0%	09-Dec-26	20-Dec-26	16-Jan-27	26-Jan-27	0.00	0.00	1,233,296.81	-32
MLTX-02-005-CI	Air Ducts and Grills Installation (Air Dome)	10	0%	0%	09-Dec-26	20-Dec-26	16-Jan-27	26-Jan-27	0.00	0.00	728,766.30	-32
MLTX-02-005-CI	Air Units Installation (Air Dome)	10	0%	0%	09-Dec-26	20-Dec-26	16-Jan-27	26-Jan-27	0.00	0.00	336,353.67	-32
MLTX-02-005-CI	Exhaust Fans and Ducts Installation (Air Dome)	10	0%	0%	09-Dec-26	20-Dec-26	16-Jan-27	26-Jan-27	0.00	0.00	168,176.84	-32
ELECTRICAL WORKS		10	0%	0%	13-Dec-26	20-Dec-26	19-Jan-27	30-Jan-27	0.00	0.00	1,513,591.54	-35

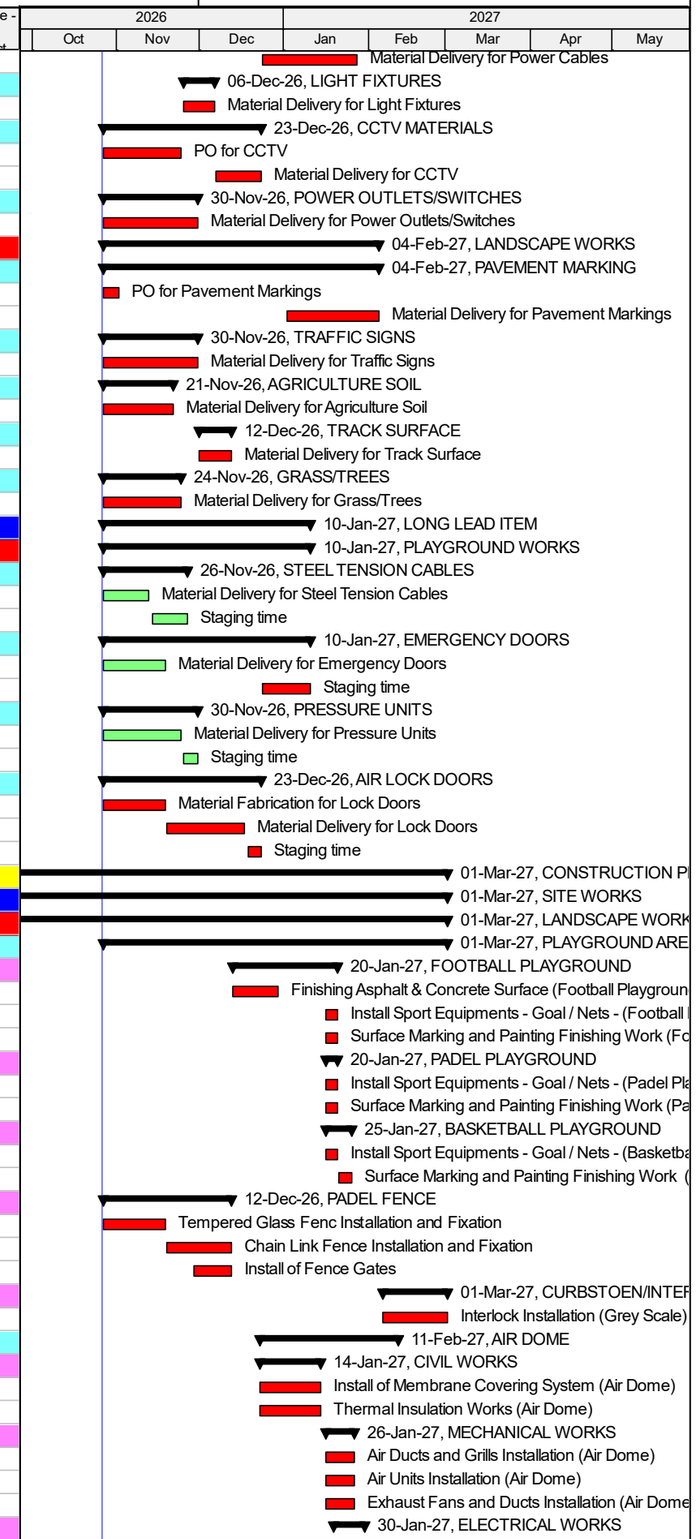

Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary


TASK filter: Remaining works.

© Oracle Corporation

MLTX-02-005 - Playground Initiative for Eastern Region (Arar-Hasa osis -Dammam)

Remaining work
D.D 26-10-2026

Activity ID	Activity Name	Original Duration	Schedule % Complete	Performance % Complete	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Variance - BL Project
MLTX-02-005-CI	Light Fixture Works (Air Dome)	7	0%	0%	13-Dec-26	20-Dec-26	19-Jan-27	26-Jan-27	0.00	0.00	224,235.78	-32
MLTX-02-005-CI	Distribution Board and Electrical Works (Air Dome)	5	0%	0%	15-Dec-26	20-Dec-26	21-Jan-27	26-Jan-27	0.00	0.00	168,176.84	-32
MLTX-02-005-CI	External Electrical Connection Works (Air Dome)	5	0%	0%	15-Dec-26	20-Dec-26	21-Jan-27	26-Jan-27	0.00	0.00	168,176.84	-32
MLTX-02-005-CI	Emergency Generator Installation (Air Dome)	3	0%	0%	17-Dec-26	20-Dec-26	24-Jan-27	26-Jan-27	0.00	0.00	504,530.51	-32
MLTX-02-005-CI	Control System Installation (Air Dome)	2	0%	0%	19-Dec-26	20-Dec-26	28-Jan-27	30-Jan-27	0.00	0.00	448,471.57	-35
FINISHES WORKS		6	0%	0%	15-Dec-26	21-Dec-26	06-Feb-27	11-Feb-27	0.00	0.00	168,176.84	-45
MLTX-02-005-CI	Doors Installation Including Emergency, Entrance doors (Air	5	0%	0%	15-Dec-26	20-Dec-26	06-Feb-27	10-Feb-27	0.00	0.00	112,117.89	-45
MLTX-02-005-CI	Logo and Signs Installation (Air Dome)	1	0%	0%	21-Dec-26	21-Dec-26	11-Feb-27	11-Feb-27	0.00	0.00	56,058.95	-45
IRRIGATION NETWORK		3	0%	0%	28-Nov-26	30-Nov-26	03-Jan-27	05-Jan-27	0.00	0.00	25,106.20	-31
MLTX-02-005-CN-1	Installing of Bubblers and Spreyers	3	0%	0%	28-Nov-26	30-Nov-26	03-Jan-27	05-Jan-27	0.00	0.00	25,106.20	-31
NATURAL GROUND		12	0%	0%	17-Nov-26	30-Nov-26	23-Dec-26	05-Jan-27	0.00	0.00	191,740.00	-31
MLTX-02-005-CN-1	Tartan Floor Installation Works for Landscape (Including	6	0%	0%	24-Nov-26	30-Nov-26	30-Dec-26	05-Jan-27	0.00	0.00	126,740.00	-31
MLTX-02-005-CN-1	Compacted Natural Ground Soil Installation Works for	6	0%	0%	17-Nov-26	23-Nov-26	23-Dec-26	29-Dec-26	0.00	0.00	65,000.00	-31
PLANTING		15	59.18%	0%	17-Sep-26	31-Oct-26	01-Dec-26	17-Dec-26	205,518.96	0.00	347,251.46	-41
MLTX-02-005-CN-1	Placement of Sweet/Agricultural Soil (Including Levelling and	6	100%	0%	17-Sep-26	24-Sep-26	01-Dec-26	07-Dec-26	104,175.44	0.00	104,175.44	-63
MLTX-02-005-CN-1	Placement of Lawn Ground Cover (Rolling and Compaction)	4	0%	0%	27-Oct-26	31-Oct-26	14-Dec-26	17-Dec-26	0.00	0.00	141,732.50	-41
MLTX-02-005-CN-1	Placement and Fixation of Trees	5	100%	0%	26-Sep-26	30-Sep-26	08-Dec-26	13-Dec-26	101,343.52	0.00	101,343.52	-63
WALKING/BIKE PATHS		24	79.59%	50%	05-Oct-26	01-Nov-26	11-Jun-26 A	13-Dec-26	292,600.66	183,816.95	367,633.90	-35
MLTX-02-005-CN-1	Bike Path Preparation and Installation Works	12	100%	50%	05-Oct-26	18-Oct-26	11-Jun-26 A	13-Dec-26	187,554.12	93,777.06	187,554.12	-47
MLTX-02-005-CN-1	Walking Path Preparation and Installation Works	12	58.33%	50%	19-Oct-26	01-Nov-26	11-Jun-26 A	13-Dec-26	105,046.54	90,039.89	180,079.78	-35
GENERAL/FURNITURE		47	0%	22.3%	27-Oct-26	30-Dec-26	18-Oct-26 A	04-Feb-27	0.00	88,036.20	394,811.80	-31
MLTX-02-005-CN-1	Stamped Concrete Works for LandScape (Including	5	0%	0%	02-Nov-26	07-Nov-26	13-Dec-26	17-Dec-26	0.00	0.00	93,594.00	-35
MLTX-02-005-CN-1	Traffic Signs Posts and Poles Installation	15	0%	0%	14-Dec-26	30-Dec-26	19-Jan-27	04-Feb-27	0.00	0.00	9,749.30	-31
MLTX-02-005-CN-1	Fixation and Installation of Steel Frame for Benches	7	0%	0%	27-Oct-26	03-Nov-26	13-Dec-26	20-Dec-26	0.00	0.00	17,274.79	-40
MLTX-02-005-CN-1	Fixation and Installation of Benches	7	0%	0%	23-Nov-26	30-Nov-26	21-Dec-26	28-Dec-26	0.00	0.00	40,307.84	-24
MLTX-02-005-CN-1	Fixation and Installation of Precast Concrete Seats	7	0%	0%	23-Nov-26	30-Nov-26	21-Dec-26	28-Dec-26	0.00	0.00	32,757.76	-24
MLTX-02-005-CN-1	Fixation and Installation of Precast Concrete Seats (Circular)	7	0%	0%	23-Nov-26	30-Nov-26	21-Dec-26	28-Dec-26	0.00	0.00	12,869.04	-24
MLTX-02-005-CN-1	Fixation and Installation of Precast Concrete Trash Bins	11	0%	0%	01-Dec-26	13-Dec-26	06-Jan-27	18-Jan-27	0.00	0.00	12,186.67	-31
MLTX-02-005-CN-1	Installing of Site Light Poles	13	0%	50%	08-Nov-26	22-Nov-26	18-Oct-26 A	10-Nov-26	0.00	88,036.20	176,072.40	10
TOILET/SERVICE BUILDING		113	32.93%	9.93%	13-Sep-26	19-Dec-26	03-Oct-26 A	23-Jan-27	176,660.98	53,282.89	536,523.00	-30
THERMAL & MOISTER PROTECTION		8	100%	90%	13-Sep-26	21-Sep-26	03-Oct-26 A	04-Nov-26	16,607.28	14,946.55	16,607.28	-37
MLTX-02-005-CN-11C	Finalize Water Proofing Works for Roofing and Wet Areas	8	100%	90%	13-Sep-26	21-Sep-26	03-Oct-26 A	04-Nov-26	16,607.28	14,946.55	16,607.28	-37
MECHANICAL WORK		77	27.54%	4.57%	29-Sep-26	19-Dec-26	22-Oct-26 A	21-Jan-27	36,762.98	6,093.32	133,476.12	-29
HVAC SYSTEM		3	0%	0%	05-Dec-26	07-Dec-26	10-Jan-27	12-Jan-27	0.00	0.00	14,623.96	-31
MLTX-02-005-CN-1	Install and Finish HVAC and Ventilation Works Including Split	3	0%	0%	05-Dec-26	07-Dec-26	10-Jan-27	12-Jan-27	0.00	0.00	14,623.96	-31
WATER SUPPLY SYSTEM		7	0%	0%	12-Dec-26	19-Dec-26	14-Jan-27	21-Jan-27	0.00	0.00	48,746.52	-29
MLTX-02-005-CN-1	Installing of Booster Pump Units Including fittings and	7	0%	0%	12-Dec-26	19-Dec-26	14-Jan-27	21-Jan-27	0.00	0.00	48,746.52	-29
SEWER/DRAINAGE SYSTEM		73	53.94%	8.94%	29-Sep-26	12-Dec-26	22-Oct-26 A	17-Jan-27	36,762.98	6,093.32	68,155.77	-31
MLTX-02-005-CN-1	Installing UPVC Pipes for External Connection for Sewage	4	100%	0%	05-Oct-26	08-Oct-26	02-Nov-26	05-Nov-26	14,217.67	0.00	14,217.67	-24
MLTX-02-005-CN-1	Installing of Plumping Fixtures and Accessories	2	100%	0%	15-Oct-26	17-Oct-26	07-Nov-26	08-Nov-26	10,358.68	0.00	10,358.68	-19
MLTX-02-005-CN-1	Installing Inspection Chamber for Sewage Network	5	100%	50%	29-Sep-26	04-Oct-26	22-Oct-26 A	01-Nov-26	12,186.63	6,093.32	12,186.63	-24
MLTX-02-005-CN-1	Installing of Toilet Fixtures and Accessories Such as Closets	4	0%	0%	08-Dec-26	12-Dec-26	13-Jan-27	17-Jan-27	0.00	0.00	31,392.79	-31
FIRE PROTECTION		2	0%	0%	14-Dec-26	15-Dec-26	13-Jan-27	14-Jan-27	0.00	0.00	1,949.87	-26
MLTX-02-005-CN-1	Installing of Fire Fighting Extinguisher and accessories	2	0%	0%	14-Dec-26	15-Dec-26	13-Jan-27	14-Jan-27	0.00	0.00	1,949.87	-26
ELECTRICAL WORKS		32	0%	0%	09-Nov-26	19-Dec-26	17-Dec-26	23-Jan-27	0.00	0.00	180,781.27	-30
FIXTURE WORKS		32	0%	0%	09-Nov-26	19-Dec-26	17-Dec-26	23-Jan-27	0.00	0.00	180,781.27	-30
MLTX-02-005-CN-1	Installing and Finish Works of Panel Boards	5	0%	0%	09-Nov-26	14-Nov-26	17-Dec-26	22-Dec-26	0.00	0.00	102,367.69	-33
MLTX-02-005-CN-1	Installing Data and Telecommunication System with all	4	0%	0%	13-Dec-26	16-Dec-26	10-Jan-27	13-Jan-27	0.00	0.00	6,239.59	-24
MLTX-02-005-CN-1	Installing and Finalize Works of Sockets and Power Points	4	0%	0%	07-Dec-26	10-Dec-26	10-Jan-27	13-Jan-27	0.00	0.00	7,085.10	-29
MLTX-02-005-CN-1	Installing and Finalize Works of Earthing Works	3	0%	0%	01-Dec-26	03-Dec-26	06-Jan-27	09-Jan-27	0.00	0.00	6,824.51	-31
MLTX-02-005-CN-1	Installing of Fire automation and Fire Alarm System	4	0%	0%	15-Dec-26	19-Dec-26	19-Jan-27	23-Jan-27	0.00	0.00	34,317.53	-30
MLTX-02-005-CN-1	Installing and Finalize Works of Lighting Works including Light	4	0%	0%	07-Dec-26	10-Dec-26	10-Jan-27	13-Jan-27	0.00	0.00	14,259.43	-29
MLTX-02-005-CN-1	Installing and Finalize Works of Lightning Protection System	6	0%	0%	05-Dec-26	10-Dec-26	10-Jan-27	16-Jan-27	0.00	0.00	2,437.33	-31
MLTX-02-005-CN-1	Installing and Finalize Works of Security and Access Control	4	0%	0%	05-Dec-26	08-Dec-26	10-Jan-27	13-Jan-27	0.00	0.00	7,250.09	-31
DOORS/WINDOWS		71	90%	0%	17-Sep-26	12-Dec-26	27-Oct-26	17-Jan-27	52,646.24	0.00	58,495.82	-31
MLTX-02-005-CN-111	Preliminary Works For Windows/Curtain Wall	2	100%	0%	17-Sep-26	19-Sep-26	27-Oct-26	28-Oct-26	52,646.24	0.00	52,646.24	-33
MLTX-02-005-CN-111	Finalize Glazzed Curtain Wall Works	7	0%	0%	05-Dec-26	12-Dec-26	10-Jan-27	17-Jan-27	0.00	0.00	5,849.58	-31
METAL WORKS		4	100%	0%	14-Sep-26	17-Sep-26	27-Oct-26	31-Oct-26	3,899.72	0.00	3,899.72	-36
MLTX-02-005-CN-111	Installation of DI Cover for Tank	4	100%	0%	14-Sep-26	17-Sep-26	27-Oct-26	31-Oct-26	3,899.72	0.00	3,899.72	-36
FINISHING WORKS		76	61.49%	38.04%	06-Oct-26	12-Dec-26	20-Oct-26 A	17-Jan-27	52,120.80	32,243.02	84,766.96	-31
FLOOR FINISHES		71	71.43%	0%	06-Oct-26	12-Dec-26	27-Oct-26	17-Jan-27	2,924.82	0.00	4,094.76	-31
MLTX-02-005-CN-1	Granite Tiles Floor Finish Works	4	100%	0%	06-Oct-26	10-Oct-26	27-Oct-26	31-Oct-26	2,924.82	0.00	2,924.82	-18
MLTX-02-005-CN-1	Epoxy Coat on Concrete Floor	3	0%	0%	09-Dec-26	12-Dec-26	14-Jan-27	17-Jan-27	0.00	0.00	1,169.94	-31
WALL FINISHES		35	60.98%	39.97%	06-Oct-26	08-Nov-26	20-Oct-26 A	30-Nov-26	49,195.98	32,243.02	80,672.20	-19

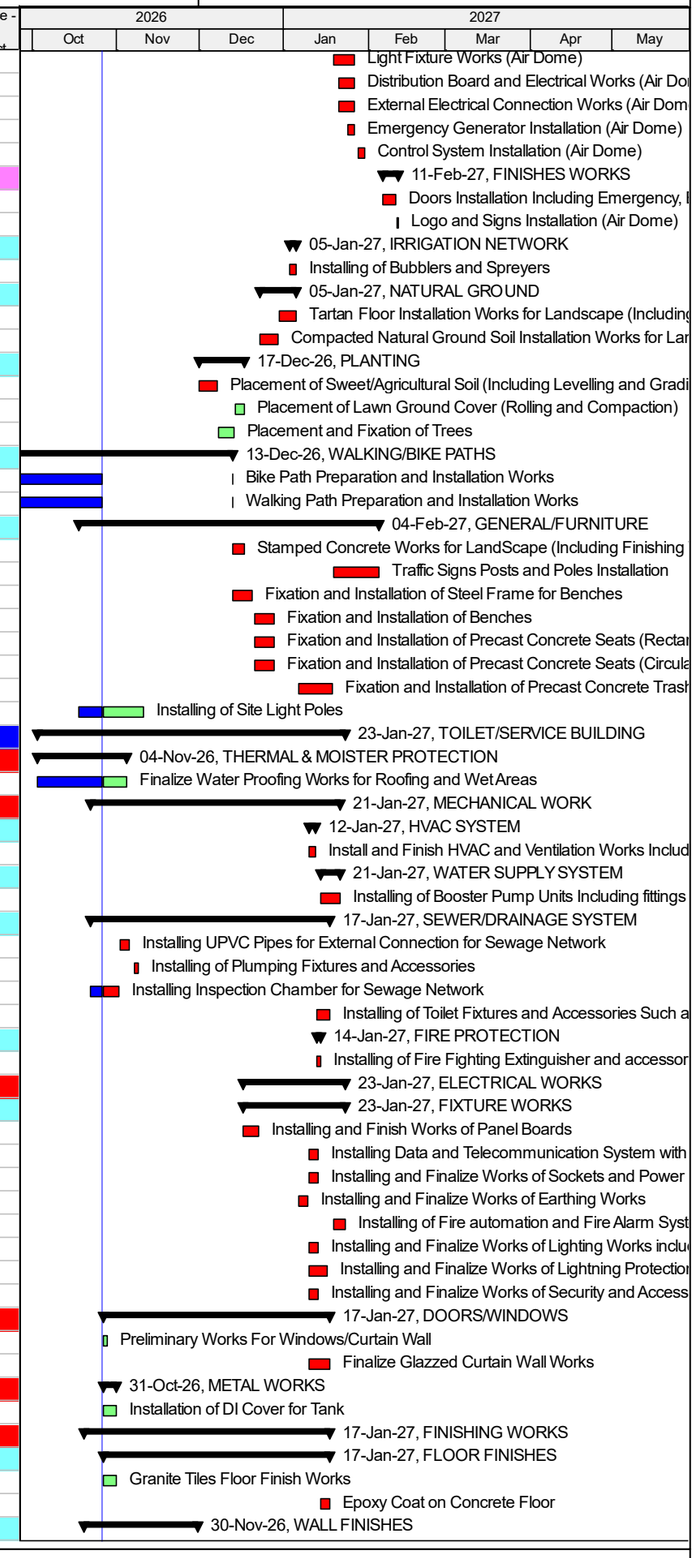

Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary

TASK filter: Remaining works.

© Oracle Corporation

MLTX-02-005 - Playground Initiative for Eastern Region (Arar-Hasa osis -Dammam)


Remaining work
D.D 26-10-2026

PROFAST شركة برو فاست المحدودة

egis

MODON مدن

Activity ID	Activity Name	Original Duration	Schedule % Complete	Performance % Complete	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Variance - BL Project
MLTX-02-005-CN-1	Glass Partitions including all accessories and doors	7	0%	0%	01-Nov-26	08-Nov-26	23-Nov-26	30-Nov-26	0.00	0.00	13,649.02	-19
MLTX-02-005-CN-1	Painting Finish Works for External Walls	7	100%	90%	06-Oct-26	13-Oct-26	20-Oct-26 A	03-Nov-26	35,825.58	32,243.02	35,825.58	-18
MLTX-02-005-CN-1	Phenolic Partitions for Toilets	7	42.86%	0%	24-Oct-26	31-Oct-26	15-Nov-26	22-Nov-26	13,370.40	0.00	31,197.60	-19
SPECIALTIES WORK		64	25%	0%	18-Oct-26	17-Dec-26	09-Nov-26	21-Jan-27	14,623.96	0.00	58,495.83	-30
MLTX-02-005-CN-113	Installation of Phenolic Locker	3	0%	0%	15-Dec-26	17-Dec-26	19-Jan-27	21-Jan-27	0.00	0.00	24,373.26	-30
MLTX-02-005-CN-113	Sanitary Fixtures and Accessories Works	5	100%	0%	18-Oct-26	22-Oct-26	09-Nov-26	14-Nov-26	14,623.96	0.00	14,623.96	-19
MLTX-02-005-CN-114	Installation of MODON Logo on the entrance	3	0%	0%	12-Dec-26	14-Dec-26	16-Jan-27	18-Jan-27	0.00	0.00	19,498.61	-30
TESTING & COMMISSIONING		31	0%	0%	20-Dec-26	02-Jan-27	24-Jan-27	01-Mar-27	0.00	0.00	0.00	-49
MLTX-02-005-TC-11860	Testing and Commissioning for MEP Works for Playground	2	0%	0%	30-Dec-26	31-Dec-26	28-Feb-27	01-Mar-27	0.00	0.00	0.00	-50
MLTX-02-005-TC-11870	Testing and Commissioning for MEP Works for Toilet/Service	12	0%	0%	20-Dec-26	02-Jan-27	24-Jan-27	06-Feb-27	0.00	0.00	0.00	-30
MLTX-02-005-TC-11880	Testing and Commissioning for MEP Works for Landscape	5	0%	0%	27-Dec-26	31-Dec-26	31-Jan-27	04-Feb-27	0.00	0.00	0.00	-30
HASA OASIS		190	12.58%	13.69%	04-May-26	02-Jan-27	01-Jun-26 A	09-Mar-27	793,337.45	863,074.97	6,303,960.36	-56
ENGINEERING		50	0%	0%	04-May-26	25-Nov-26	27-Oct-26	23-Dec-26	0.00	0.00	0.00	-24
SHOP DRAWINGS		50	0%	0%	04-May-26	25-Nov-26	27-Oct-26	23-Dec-26	0.00	0.00	0.00	-24
SHOP DRAWINGS SUBMISSION		25	0%	0%	04-May-26	04-Jun-26	27-Oct-26	24-Nov-26	0.00	0.00	0.00	-147
SHOP DRAWINGS SUBMITTALS FOR PLAYGROUND WORKS		25	0%	0%	04-May-26	04-Jun-26	27-Oct-26	24-Nov-26	0.00	0.00	0.00	-147
ELECTRICAL WORKS		25	0%	0%	04-May-26	04-Jun-26	27-Oct-26	24-Nov-26	0.00	0.00	0.00	-147
MLTX-02-005-EI	Shop DWG Submittal for Power Layout	25	100%	0%	04-May-26	04-Jun-26	27-Oct-26	24-Nov-26	0.00	0.00	0.00	-147
SHOP DRAWINGS APPROVALS		50	0%	0%	06-Jun-26	25-Nov-26	27-Oct-26	23-Dec-26	0.00	0.00	0.00	-24
SHOP DRAWINGS APPROVAL FOR PLAYGROUND WORKS		50	0%	0%	06-Jun-26	25-Nov-26	27-Oct-26	23-Dec-26	0.00	0.00	0.00	-24
ELECTRICAL WORKS		50	0%	0%	06-Jun-26	25-Nov-26	27-Oct-26	23-Dec-26	0.00	0.00	0.00	-24
MLTX-02-005-EI	Shop DWG Approval for Power Layout	25	100%	0%	06-Jun-26	04-Jul-26	25-Nov-26	23-Dec-26	0.00	0.00	0.00	-147
MLTX-02-005-EI	Shop DWG Approval for Power Installation Details	25	0%	0%	28-Oct-26	25-Nov-26	27-Oct-26	24-Nov-26	0.00	0.00	0.00	1
PROCUREMENT		88	0%	0%	16-Jun-26	01-Dec-26	27-Oct-26	06-Feb-27	0.00	0.00	0.00	-57
SHORT LEAD ITEM		88	0%	0%	16-Jun-26	01-Dec-26	27-Oct-26	06-Feb-27	0.00	0.00	0.00	-57
TOILET/SERVICE WORKS		49	0%	0%	16-Jun-26	19-Oct-26	27-Oct-26	22-Dec-26	0.00	0.00	0.00	-55
LIGHTING FIXTURES		20	0%	0%	16-Jun-26	08-Jul-26	27-Oct-26	18-Nov-26	0.00	0.00	0.00	-113
MLTX-02-005-PR-1	Material Delivery for Lighting Fixtures	20	100%	0%	16-Jun-26	08-Jul-26	27-Oct-26	18-Nov-26	0.00	0.00	0.00	-113
SWITCHES/SOCKETS		32	0%	0%	16-Jun-26	22-Jul-26	27-Oct-26	02-Dec-26	0.00	0.00	0.00	-113
MLTX-02-005-PR-1	PO for Switches/Sockets	15	100%	0%	16-Jun-26	02-Jul-26	27-Oct-26	12-Nov-26	0.00	0.00	0.00	-113
MLTX-02-005-PR-1	Material Delivery for Switches/Sockets	17	100%	0%	04-Jul-26	22-Jul-26	14-Nov-26	02-Dec-26	0.00	0.00	0.00	-113
DISTRIBUTION PANNELS		20	0%	0%	27-Sep-26	19-Oct-26	27-Oct-26	18-Nov-26	0.00	0.00	0.00	-26
MLTX-02-005-PR-1	PO for Distribution Panels	5	100%	0%	27-Sep-26	01-Oct-26	27-Oct-26	01-Nov-26	0.00	0.00	0.00	-26
MLTX-02-005-PR-1	Material Delivery for Distribution Panels	15	100%	0%	03-Oct-26	19-Oct-26	02-Nov-26	18-Nov-26	0.00	0.00	0.00	-26
FURNITURES		49	0%	0%	16-Jun-26	11-Aug-26	27-Oct-26	22-Dec-26	0.00	0.00	0.00	-113
MLTX-02-005-PR-1	PO for Furnitures	19	100%	0%	16-Jun-26	07-Jul-26	27-Oct-26	17-Nov-26	0.00	0.00	0.00	-113
MLTX-02-005-PR-1	Material Delivery for Furnitures	30	100%	0%	08-Jul-26	11-Aug-26	18-Nov-26	22-Dec-26	0.00	0.00	0.00	-113
PLAYGROUND WORKS		88	0%	0%	28-Jun-26	01-Dec-26	27-Oct-26	06-Feb-27	0.00	0.00	0.00	-57
PVC MEMBRANE		30	0%	0%	29-Sep-26	02-Nov-26	14-Nov-26	17-Dec-26	0.00	0.00	0.00	-39
MLTX-02-005-PR-1	Material Delivery for PVC Membrane	30	80%	0%	29-Sep-26	02-Nov-26	14-Nov-26	17-Dec-26	0.00	0.00	0.00	-39
ARTIFICIAL TURF		30	0%	0%	30-Sep-26	03-Nov-26	27-Oct-26	30-Nov-26	0.00	0.00	0.00	-23
MLTX-02-005-PR-1	Material Delivery for Artificial TURF	30	76.67%	0%	30-Sep-26	03-Nov-26	27-Oct-26	30-Nov-26	0.00	0.00	0.00	-23
RUBBER GRANULES		30	0%	0%	20-Sep-26	25-Oct-26	27-Oct-26	30-Nov-26	0.00	0.00	0.00	-31
MLTX-02-005-PR-1	Material Delivery for Rubber Granules	30	100%	0%	20-Sep-26	25-Oct-26	27-Oct-26	30-Nov-26	0.00	0.00	0.00	-31
PADEL GLASS		30	0%	0%	16-Sep-26	21-Oct-26	27-Oct-26	30-Nov-26	0.00	0.00	0.00	-34
MLTX-02-005-PR-1	Material Delivery for Padel Glass	30	100%	0%	16-Sep-26	21-Oct-26	27-Oct-26	30-Nov-26	0.00	0.00	0.00	-34
PADEL WIRE MESH/STEEL SETS		15	0%	0%	16-Sep-26	04-Oct-26	27-Oct-26	12-Nov-26	0.00	0.00	0.00	-34
MLTX-02-005-PR-1	Material Delivery for Wire Mesh/Steel Sets	15	100%	0%	16-Sep-26	04-Oct-26	27-Oct-26	12-Nov-26	0.00	0.00	0.00	-34
MARKING PAINT		32	0%	0%	28-Jun-26	03-Aug-26	27-Oct-26	02-Dec-26	0.00	0.00	0.00	-103
MLTX-02-005-PR-1	PO for Marking Paint	15	100%	0%	28-Jun-26	14-Jul-26	27-Oct-26	12-Nov-26	0.00	0.00	0.00	-103
MLTX-02-005-PR-1	Material Delivery for Marking Paint	17	100%	0%	15-Jul-26	03-Aug-26	14-Nov-26	02-Dec-26	0.00	0.00	0.00	-103
AIR DIFUSSERS/GRILLS		40	0%	0%	24-Sep-26	09-Nov-26	27-Oct-26	12-Dec-26	0.00	0.00	0.00	-28
MLTX-02-005-PR-1	PO for Air Difussers/Grills	15	100%	0%	24-Sep-26	11-Oct-26	27-Oct-26	12-Nov-26	0.00	0.00	0.00	-28
MLTX-02-005-PR-1	Material Delivery for Air Difussers/Grills	25	52%	0%	12-Oct-26	09-Nov-26	14-Nov-26	12-Dec-26	0.00	0.00	0.00	-28
GALVANIZED DUCTS		40	0%	0%	24-Sep-26	09-Nov-26	27-Oct-26	12-Dec-26	0.00	0.00	0.00	-28
MLTX-02-005-PR-1	PO for Galvanized Duct	15	100%	0%	24-Sep-26	11-Oct-26	27-Oct-26	12-Nov-26	0.00	0.00	0.00	-28
MLTX-02-005-PR-1	Material Delivery for Galvanized Duct	25	52%	0%	12-Oct-26	09-Nov-26	14-Nov-26	12-Dec-26	0.00	0.00	0.00	-28
EXHAUST FANS		40	0%	0%	10-Sep-26	02-Nov-26	27-Oct-26	12-Dec-26	0.00	0.00	0.00	-34
MLTX-02-005-PR-1	PO for Exhaust Fans	15	100%	0%	10-Sep-26	28-Sep-26	27-Oct-26	12-Nov-26	0.00	0.00	0.00	-39
MLTX-02-005-PR-1	Material Delivery for Exhaust Fans	25	76%	0%	05-Oct-26	02-Nov-26	14-Nov-26	12-Dec-26	0.00	0.00	0.00	-34
DISTRIBUTION BOARDS		20	0%	0%	10-Oct-26	01-Nov-26	14-Nov-26	06-Dec-26	0.00	0.00	0.00	-30
MLTX-02-005-PR-1	PO for Distribution Boards	5	100%	0%	10-Oct-26	14-Oct-26	14-Nov-26	18-Nov-26	0.00	0.00	0.00	-30
MLTX-02-005-PR-1	Material Delivery for Distribution Boards	15	66.67%	0%	15-Oct-26	01-Nov-26	19-Nov-26	06-Dec-26	0.00	0.00	0.00	-30
POWER CABLES		35	0%	0%	22-Oct-26	01-Dec-26	01-Dec-26	10-Jan-27	0.00	0.00	0.00	-34

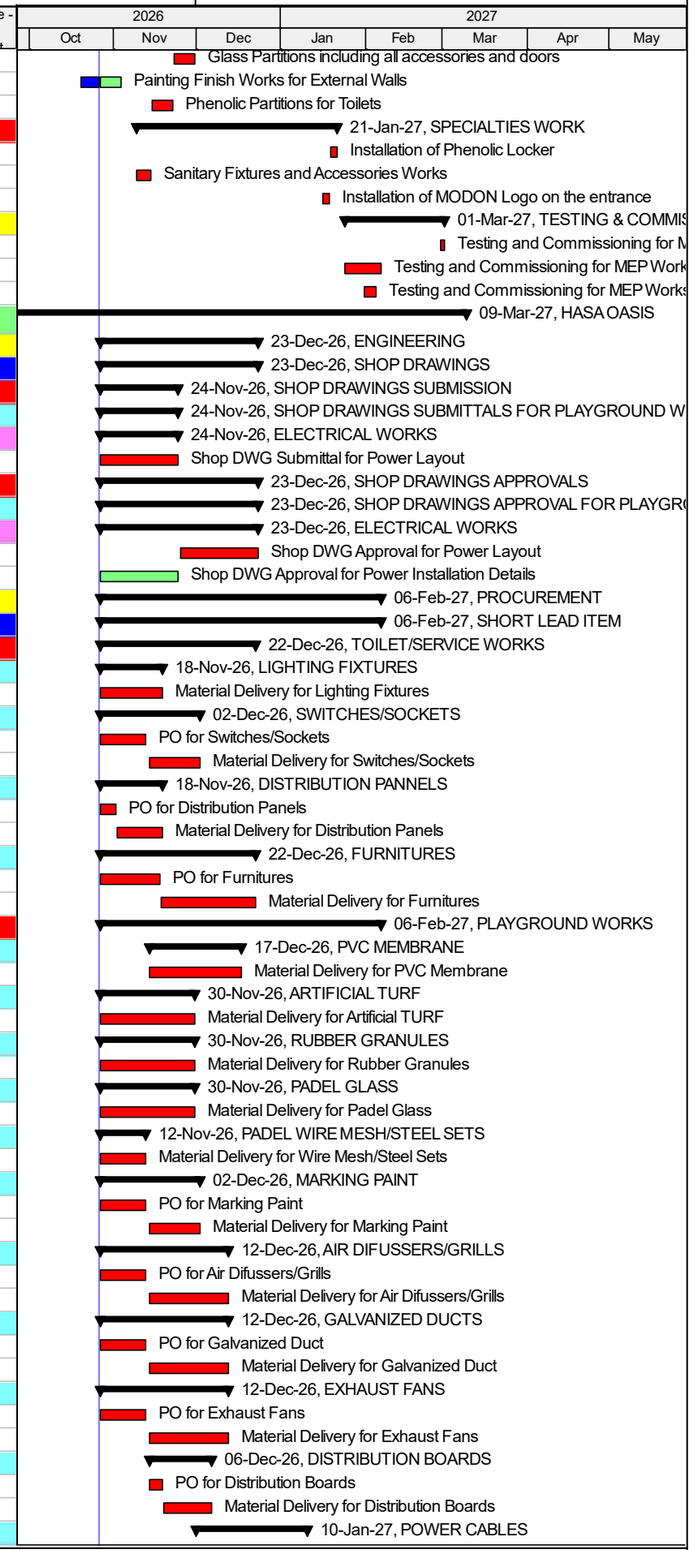

Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary


TASK filter: Remaining works.

© Oracle Corporation

MLTX-02-005 - Playground Initiative for Eastern Region (Arar-Hasa osis -Dammam)

Remaining work
D.D 26-10-2026

Activity ID	Activity Name	Original Duration	Schedule % Complete	Performance % Complete	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Variance - BL Project
MLTX-02-005-PR-1	PO for Power Cables	15	26.67%	0%	22-Oct-26	08-Nov-26	01-Dec-26	17-Dec-26	0.00	0.00	0.00	-34
MLTX-02-005-PR-1	Material Delivery for Power Cables	20	0%	0%	09-Nov-26	01-Dec-26	19-Dec-26	10-Jan-27	0.00	0.00	0.00	-34
LIGHT FIXTURES		20	0%	0%	09-Nov-26	01-Dec-26	19-Dec-26	10-Jan-27	0.00	0.00	0.00	-34
MLTX-02-005-PR-1	Material Delivery for Light Fixtures	20	0%	0%	09-Nov-26	01-Dec-26	19-Dec-26	10-Jan-27	0.00	0.00	0.00	-34
CCTV MATERIALS		88	0%	0%	04-Jul-26	29-Nov-26	27-Oct-26	06-Feb-27	0.00	0.00	0.00	-59
MLTX-02-005-PR-1	PO for CCTV	15	100%	0%	04-Jul-26	20-Jul-26	27-Oct-26	12-Nov-26	0.00	0.00	0.00	-98
MLTX-02-005-PR-1	Material Delivery for CCTV	15	0%	0%	12-Nov-26	29-Nov-26	20-Jan-27	06-Feb-27	0.00	0.00	0.00	-59
POWER OUTLETS/SWITCHES		41	0%	0%	23-Jul-26	10-Nov-26	03-Dec-26	19-Jan-27	0.00	0.00	0.00	-60
MLTX-02-005-PR-1	PO for Power Outlets/Switches	16	100%	0%	23-Jul-26	10-Aug-26	03-Dec-26	21-Dec-26	0.00	0.00	0.00	-113
MLTX-02-005-PR-1	Material Delivery for Power Outlets/Switches	25	48%	0%	13-Oct-26	10-Nov-26	22-Dec-26	19-Jan-27	0.00	0.00	0.00	-60
LANDSCAPE WORKS		81	0%	0%	11-Aug-26	04-Nov-26	27-Oct-26	28-Jan-27	0.00	0.00	0.00	-73
PAVEMENT MARKING		33	0%	0%	11-Aug-26	04-Nov-26	22-Dec-26	28-Jan-27	0.00	0.00	0.00	-73
MLTX-02-005-PR-1	PO for Pavement Markings	13	100%	0%	11-Aug-26	25-Aug-26	22-Dec-26	05-Jan-27	0.00	0.00	0.00	-113
MLTX-02-005-PR-1	Material Delivery for Pavement Markings	20	60%	0%	13-Oct-26	04-Nov-26	06-Jan-27	28-Jan-27	0.00	0.00	0.00	-73
TRAFFIC SIGNS		5	0%	0%	21-Sep-26	27-Sep-26	27-Oct-26	01-Nov-26	0.00	0.00	0.00	-30
MLTX-02-005-PR-1	Material Delivery for Traffic Signs	5	100%	0%	21-Sep-26	27-Sep-26	27-Oct-26	01-Nov-26	0.00	0.00	0.00	-30
TRACK SURFACE		2	0%	0%	29-Aug-26	30-Aug-26	06-Jan-27	07-Jan-27	0.00	0.00	0.00	-111
MLTX-02-005-PR-1	Material Delivery for Track Surface	2	100%	0%	29-Aug-26	30-Aug-26	06-Jan-27	07-Jan-27	0.00	0.00	0.00	-111
GRASS/TREES		25	0%	0%	28-Sep-26	26-Oct-26	27-Oct-26	24-Nov-26	0.00	0.00	0.00	-25
MLTX-02-005-PR-1	Material Delivery for Grass/Trees	25	100%	0%	28-Sep-26	26-Oct-26	27-Oct-26	24-Nov-26	0.00	0.00	0.00	-25
LONG LEAD ITEM		45	0%	0%	15-Jul-26	16-Nov-26	27-Oct-26	17-Dec-26	0.00	0.00	0.00	-27
PLAYGROUND WORKS		45	0%	0%	15-Jul-26	16-Nov-26	27-Oct-26	17-Dec-26	0.00	0.00	0.00	-27
STEEL TENSION CABLES		26	0%	0%	21-Sep-26	21-Oct-26	27-Oct-26	25-Nov-26	0.00	0.00	0.00	-30
MLTX-02-005-PR-1	Material Delivery for Steel Tension Cables	16	100%	0%	21-Sep-26	10-Oct-26	27-Oct-26	14-Nov-26	0.00	0.00	0.00	-30
MLTX-02-005-PR-1	Staging time	10	100%	0%	11-Oct-26	21-Oct-26	15-Nov-26	25-Nov-26	0.00	0.00	0.00	-30
EMERGENCY DOORS		30	0%	0%	15-Jul-26	18-Aug-26	14-Nov-26	17-Dec-26	0.00	0.00	0.00	-103
MLTX-02-005-PR-1	Material Delivery for Emergency Doors	25	100%	0%	15-Jul-26	12-Aug-26	14-Nov-26	12-Dec-26	0.00	0.00	0.00	-103
MLTX-02-005-PR-1	Staging time	5	100%	0%	13-Aug-26	18-Aug-26	13-Dec-26	17-Dec-26	0.00	0.00	0.00	-103
PRESSURE UNITS		30	0%	0%	13-Oct-26	16-Nov-26	27-Oct-26	30-Nov-26	0.00	0.00	0.00	-12
MLTX-02-005-PR-1	Material Delivery for Pressure Units	25	48%	0%	13-Oct-26	10-Nov-26	27-Oct-26	24-Nov-26	0.00	0.00	0.00	-12
MLTX-02-005-PR-1	Staging time	5	0%	0%	11-Nov-26	16-Nov-26	25-Nov-26	30-Nov-26	0.00	0.00	0.00	-12
AIR LOCK DOORS		31	0%	0%	03-Oct-26	05-Nov-26	27-Oct-26	01-Dec-26	0.00	0.00	0.00	-22
MLTX-02-005-PR-1	Material Delivery for Lock Doors	25	84%	0%	03-Oct-26	31-Oct-26	27-Oct-26	24-Nov-26	0.00	0.00	0.00	-21
MLTX-02-005-PR-1	Staging time	5	0%	0%	01-Nov-26	05-Nov-26	26-Nov-26	01-Dec-26	0.00	0.00	0.00	-22
CONSTRUCTION PHASE		190	12.58%	13.69%	30-Jul-26	31-Dec-26	01-Jun-26 A	15-Feb-27	793,337.45	863,074.97	6,303,960.36	-39
SITE WORKS		135	11.86%	13.42%	29-Sep-26	31-Dec-26	01-Jun-26 A	15-Feb-27	700,096.91	792,292.07	5,901,888.43	-39
LANDSCAPE WORKS		135	11.86%	13.42%	29-Sep-26	31-Dec-26	01-Jun-26 A	15-Feb-27	700,096.91	792,292.07	5,901,888.43	-39
PLAYGROUND AREA		114	40.56%	32.45%	29-Sep-26	31-Dec-26	21-Sep-26 A	08-Feb-27	180,520.67	144,416.54	445,050.38	-33
FOOTBALL PLAYGROUND		24	0%	0%	17-Nov-26	09-Dec-26	29-Nov-26	26-Dec-26	0.00	0.00	47,527.50	-14
MLTX-02-005-CI	Install Sport Equipments - Goal / Nets - (Football Playground)	20	0%	0%	17-Nov-26	09-Dec-26	29-Nov-26	21-Dec-26	0.00	0.00	31,685.00	-10
MLTX-02-005-CI	Surface Marking and Painting (Football Playground)	3	0%	0%	17-Nov-26	19-Nov-26	23-Dec-26	26-Dec-26	0.00	0.00	15,842.50	-31
PADEL PLAYGROUND		18	0%	0%	12-Dec-26	31-Dec-26	27-Dec-26	16-Jan-27	0.00	0.00	70,195.20	-13
MLTX-02-005-CI	Install Sport Equipments - Goal / Nets - (Padel Playground)	15	0%	0%	12-Dec-26	28-Dec-26	27-Dec-26	12-Jan-27	0.00	0.00	58,496.00	-13
MLTX-02-005-CI	Surface Marking and Painting (Padel Playground)	3	0%	0%	29-Dec-26	31-Dec-26	13-Jan-27	16-Jan-27	0.00	0.00	11,699.20	-13
BASKETBALL PLAYGROUND		42	0%	0%	17-Nov-26	31-Dec-26	29-Nov-26	16-Jan-27	0.00	0.00	96,956.10	-13
MLTX-02-005-CI	Install Sport Equipments - Goal / Nets - (Basketball	10	0%	0%	17-Nov-26	28-Nov-26	29-Nov-26	09-Dec-26	0.00	0.00	80,796.75	-10
MLTX-02-005-CI	Surface Marking and Painting (Basketball Playground)	3	0%	0%	29-Dec-26	31-Dec-26	13-Jan-27	16-Jan-27	0.00	0.00	16,159.35	-13
PADEL FENCE		38	0%	0%	02-Dec-26	31-Dec-26	27-Dec-26	08-Feb-27	0.00	0.00	49,850.91	-33
MLTX-02-005-CI	Tempered Glass Fenc Installation and Fixation	15	0%	0%	02-Dec-26	19-Dec-26	27-Dec-26	12-Jan-27	0.00	0.00	30,677.48	-21
MLTX-02-005-CI	Chain Link Fence Installation and Fixation	15	0%	0%	02-Dec-26	19-Dec-26	27-Dec-26	12-Jan-27	0.00	0.00	15,338.75	-21
MLTX-02-005-CI	Install of Fence Gates	26	0%	0%	02-Dec-26	31-Dec-26	10-Jan-27	08-Feb-27	0.00	0.00	3,834.68	-33
CURBSTOEN/INTERLOCK		3	100%	80%	29-Sep-26	01-Oct-26	21-Sep-26 A	29-Oct-26	180,520.67	144,416.54	180,520.67	-24
MLTX-02-005-CI	Interlock Installation (Grey Scale) for LandScape (Including	3	100%	80%	29-Sep-26	01-Oct-26	21-Sep-26 A	29-Oct-26	180,520.67	144,416.54	180,520.67	-24
AIR DOME		47	0%	0%	15-Nov-26	10-Dec-26	23-Dec-26	15-Feb-27	0.00	0.00	4,306,367.09	-57
CIVIL WORKS		20	0%	0%	15-Nov-26	07-Dec-26	23-Dec-26	14-Jan-27	0.00	0.00	1,391,301.90	-33
MLTX-02-005-CI	Install of Membrane Covering System (Air Dome)	20	0%	0%	15-Nov-26	07-Dec-26	23-Dec-26	14-Jan-27	0.00	0.00	942,830.33	-33
MLTX-02-005-CI	Thermal Insulation Works (Air Dome)	20	0%	0%	15-Nov-26	07-Dec-26	23-Dec-26	14-Jan-27	0.00	0.00	448,471.57	-33
MECHANICAL WORKS		15	0%	0%	21-Nov-26	07-Dec-26	23-Dec-26	09-Jan-27	0.00	0.00	1,233,296.81	-28
MLTX-02-005-CI	Air Ducts and Grills Installation (Air Dome)	15	0%	0%	21-Nov-26	07-Dec-26	23-Dec-26	09-Jan-27	0.00	0.00	728,766.30	-28
MLTX-02-005-CI	Air Units Installation (Air Dome)	8	0%	0%	29-Nov-26	07-Dec-26	31-Dec-26	09-Jan-27	0.00	0.00	336,353.67	-28
MLTX-02-005-CI	Exhaust Fans and Ducts Installation (Air Dome)	8	0%	0%	29-Nov-26	07-Dec-26	31-Dec-26	09-Jan-27	0.00	0.00	168,176.84	-28
ELECTRICAL WORKS		31	0%	0%	02-Dec-26	10-Dec-26	11-Jan-27	15-Feb-27	0.00	0.00	1,513,591.54	-57
MLTX-02-005-CI	Light Fixture Works (Air Dome)	8	0%	0%	02-Dec-26	10-Dec-26	11-Jan-27	19-Jan-27	0.00	0.00	224,235.78	-34
MLTX-02-005-CI	Distribution Board and Electrical Works (Air Dome)	8	0%	0%	02-Dec-26	10-Dec-26	20-Jan-27	28-Jan-27	0.00	0.00	168,176.84	-42

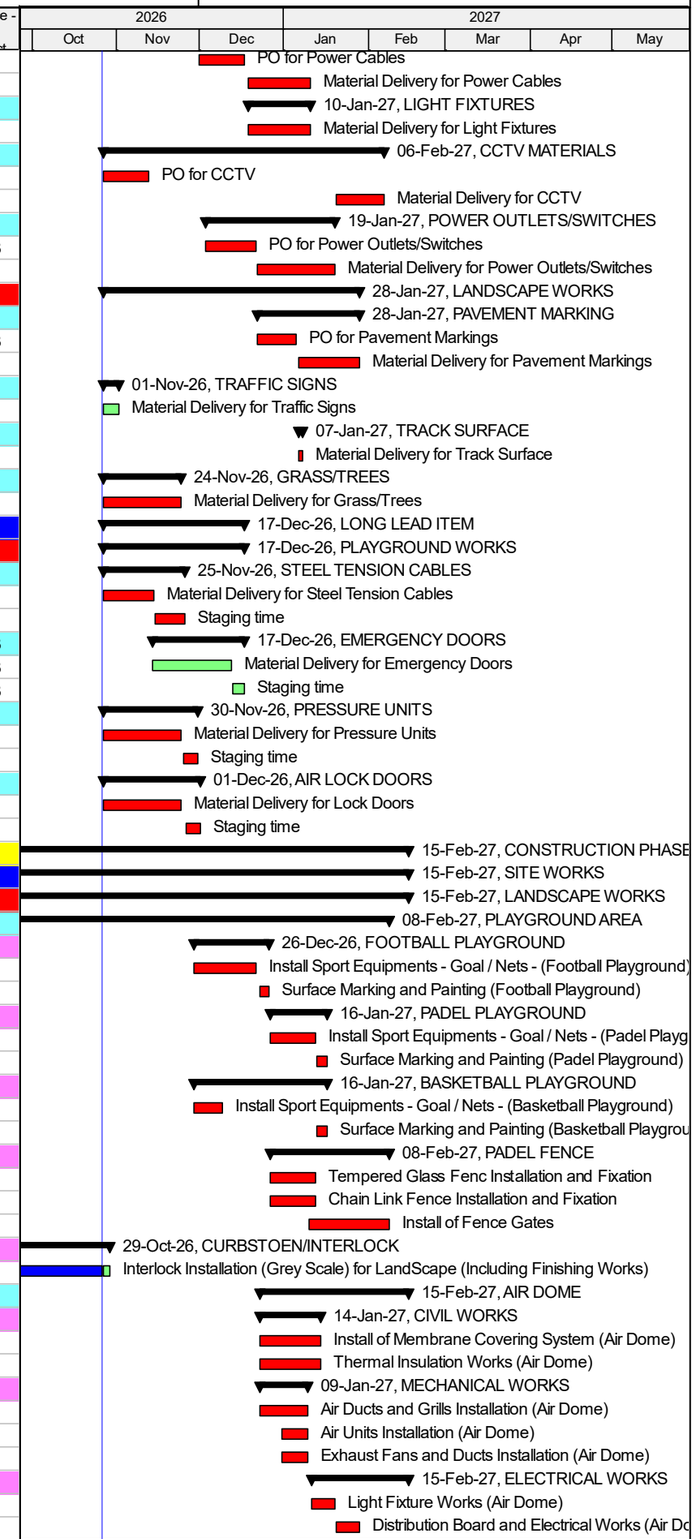

Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary


TASK filter: Remaining works.

© Oracle Corporation

MLTX-02-005 - Playground Initiative for Eastern Region (Arar-Hasa osis -Dammam)

Remaining work
D.D 26-10-2026

Activity ID	Activity Name	Original Duration	Schedule % Complete	Performance % Complete	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Variance - BL Project
MLTX-02-005-CI	External Electrical Connection Works (Air Dome)	8	0%	0%	02-Dec-26	10-Dec-26	20-Jan-27	28-Jan-27	0.00	0.00	168,176.84	-42
MLTX-02-005-CI	Emergency Generator Installation (Air Dome)	8	0%	0%	02-Dec-26	10-Dec-26	20-Jan-27	28-Jan-27	0.00	0.00	504,530.51	-42
MLTX-02-005-CI	Control System Installation (Air Dome)	8	0%	0%	02-Dec-26	10-Dec-26	07-Feb-27	15-Feb-27	0.00	0.00	448,471.57	-57
FINISHES WORKS		47	0%	0%	15-Nov-26	10-Dec-26	23-Dec-26	15-Feb-27	0.00	0.00	168,176.84	-57
MLTX-02-005-CI	Doors Installation Including Emergency, Entrance doors (Air	15	0%	0%	15-Nov-26	01-Dec-26	23-Dec-26	09-Jan-27	0.00	0.00	112,117.89	-33
MLTX-02-005-CI	Logo and Signs Installation (Air Dome)	2	0%	0%	09-Dec-26	10-Dec-26	14-Feb-27	15-Feb-27	0.00	0.00	56,058.95	-57
IRRIGATION NETWORK		3	0%	0%	05-Dec-26	07-Dec-26	27-Dec-26	29-Dec-26	0.00	0.00	25,106.20	-19
MLTX-02-005-CN-1	Installing of Bubblers and Spreyers	3	0%	0%	05-Dec-26	07-Dec-26	27-Dec-26	29-Dec-26	0.00	0.00	25,106.20	-19
NATURAL GROUND		15	0%	63.56%	29-Nov-26	07-Dec-26	13-Oct-26 A	01-Nov-26	0.00	121,870.00	191,740.00	31
MLTX-02-005-CN-1	Tartan Floor Installation Works for Landscape (Including	3	0%	50%	05-Dec-26	07-Dec-26	14-Oct-26 A	29-Oct-26	0.00	63,370.00	126,740.00	33
MLTX-02-005-CN-1	Compacted Natural Ground Soil Installation Works for	5	0%	90%	29-Nov-26	03-Dec-26	13-Oct-26 A	01-Nov-26	0.00	58,500.00	65,000.00	28
PLANTING		101	30%	56%	24-Oct-26	02-Nov-26	03-Oct-26 A	29-Oct-26	104,175.44	194,460.82	347,251.46	3
MLTX-02-005-CN-1	Placement of Sweet/Agricultural Soil (Including Levelling and	3	100%	70%	24-Oct-26	26-Oct-26	03-Oct-26 A	29-Oct-26	104,175.44	72,922.81	104,175.44	-3
MLTX-02-005-CN-1	Placement of Lawn Ground Cover (Rolling and Compaction)	3	0%	50%	31-Oct-26	02-Nov-26	14-Oct-26 A	29-Oct-26	0.00	70,866.25	141,732.50	3
MLTX-02-005-CN-1	Placement and Fixation of Trees	3	0%	50%	27-Oct-26	29-Oct-26	14-Oct-26 A	29-Oct-26	0.00	50,671.76	101,343.52	0
WALKING/BIKE PATHS		16	100%	80%	29-Sep-26	17-Oct-26	01-Jun-26 A	27-Oct-26	367,633.90	294,107.12	367,633.90	-8
MLTX-02-005-CN-1	Bike Path Preparation and Installation Works	8	100%	80%	29-Sep-26	07-Oct-26	01-Jun-26 A	27-Oct-26	187,554.12	150,043.30	187,554.12	-16
MLTX-02-005-CN-1	Walking Path Preparation and Installation Works	8	100%	80%	08-Oct-26	17-Oct-26	10-Jun-26 A	27-Oct-26	180,079.78	144,063.82	180,079.78	-8
GENERAL/FURNITURE		83	21.84%	17.12%	15-Oct-26	24-Dec-26	14-Oct-26 A	20-Jan-27	47,766.90	37,437.60	218,739.40	-23
MLTX-02-005-CN-1	Stamped Concrete Works for LandScape (Including	18	44.44%	40%	18-Oct-26	07-Nov-26	14-Oct-26 A	16-Nov-26	41,597.33	37,437.60	93,594.00	-8
MLTX-02-005-CN-1	Traffic Signs Posts and Poles Installation	3	0%	0%	20-Dec-26	22-Dec-26	16-Jan-27	18-Jan-27	0.00	0.00	9,749.30	-23
MLTX-02-005-CN-1	Fixation and Installation of Steel Frame for Benches	28	35.71%	0%	15-Oct-26	16-Nov-26	27-Oct-26	28-Nov-26	6,169.57	0.00	17,274.79	-10
MLTX-02-005-CN-1	Fixation and Installation of Benches	14	0%	0%	17-Nov-26	02-Dec-26	29-Nov-26	14-Dec-26	0.00	0.00	40,307.84	-10
MLTX-02-005-CN-1	Fixation and Installation of Precast Concrete Seats	14	0%	0%	03-Dec-26	19-Dec-26	29-Nov-26	14-Dec-26	0.00	0.00	32,757.76	4
MLTX-02-005-CN-1	Fixation and Installation of Precast Concrete Seats (Circular)	14	0%	0%	03-Dec-26	19-Dec-26	15-Dec-26	30-Dec-26	0.00	0.00	12,869.04	-10
MLTX-02-005-CN-1	Fixation and Installation of Precast Concrete Trash Bins	2	0%	0%	23-Dec-26	24-Dec-26	19-Jan-27	20-Jan-27	0.00	0.00	12,186.67	-23
TOILET/SERVICE BUILDING		190	23.19%	17.6%	30-Jul-26	23-Dec-26	20-Sep-26 A	21-Jan-27	93,240.54	70,782.89	402,071.93	-25
THERMAL & MOISTER PROTECTION		18	100%	90%	30-Jul-26	19-Aug-26	20-Sep-26 A	16-Nov-26	16,607.28	14,946.55	16,607.28	-75
MLTX-02-005-CN-126	Finalize Water Proofing Works for Roofing and Wet Areas	18	100%	90%	30-Jul-26	19-Aug-26	20-Sep-26 A	16-Nov-26	16,607.28	14,946.55	16,607.28	-75
MECHANICAL WORK		21	0%	0%	28-Nov-26	21-Dec-26	14-Dec-26	06-Jan-27	0.00	0.00	1,949.87	-14
FIRE PROTECTION		21	0%	0%	28-Nov-26	21-Dec-26	14-Dec-26	06-Jan-27	0.00	0.00	1,949.87	-14
MLTX-02-005-CN-1	Installing of Fire Fighting Extinguisher and accessories	21	0%	0%	28-Nov-26	21-Dec-26	14-Dec-26	06-Jan-27	0.00	0.00	1,949.87	-14
ELECTRICAL WORKS		52	0%	0%	04-Nov-26	21-Dec-26	19-Nov-26	18-Jan-27	0.00	0.00	180,781.27	-24
FIXTURE WORKS		52	0%	0%	04-Nov-26	21-Dec-26	19-Nov-26	18-Jan-27	0.00	0.00	180,781.27	-24
MLTX-02-005-CN-1	Installing of Fire automation and Fire Alarm System	18	0%	0%	28-Nov-26	17-Dec-26	14-Dec-26	03-Jan-27	0.00	0.00	34,317.53	-14
MLTX-02-005-CN-1	Installing and Finish Works of Panel Boards	20	0%	0%	04-Nov-26	26-Nov-26	19-Nov-26	12-Dec-26	0.00	0.00	102,367.69	-13
MLTX-02-005-CN-1	Installing and Finalize Works of Sockets and Power Points	20	0%	0%	28-Nov-26	20-Dec-26	13-Dec-26	04-Jan-27	0.00	0.00	7,085.10	-13
MLTX-02-005-CN-1	Installing and Finalize Works of Lighting Works including Light	21	0%	0%	28-Nov-26	21-Dec-26	13-Dec-26	05-Jan-27	0.00	0.00	14,259.43	-13
MLTX-02-005-CN-1	Installing Data and Telecommunication System with all	20	0%	0%	28-Nov-26	20-Dec-26	14-Dec-26	05-Jan-27	0.00	0.00	6,239.59	-14
MLTX-02-005-CN-1	Installing and Finalize Works of Security and Access Control	20	0%	0%	21-Nov-26	13-Dec-26	27-Dec-26	18-Jan-27	0.00	0.00	7,250.09	-31
MLTX-02-005-CN-1	Installing and Finalize Works of Earthing Works	20	0%	0%	28-Nov-26	20-Dec-26	13-Dec-26	04-Jan-27	0.00	0.00	6,824.51	-13
MLTX-02-005-CN-1	Installing and Finalize Works of Lightning Protection System	20	0%	0%	21-Nov-26	13-Dec-26	27-Dec-26	18-Jan-27	0.00	0.00	2,437.33	-31
DOORS/WINDOWS		115	0%	18%	21-Nov-26	16-Dec-26	24-Oct-26 A	08-Nov-26	0.00	10,529.25	58,495.82	33
MLTX-02-005-CN-130	Finalize Glazzed Curtain Wall Works	11	0%	0%	05-Dec-26	16-Dec-26	27-Oct-26	08-Nov-26	0.00	0.00	5,849.58	33
MLTX-02-005-CN-131	Preliminary Works For Windows/Curtain Wall	12	0%	20%	21-Nov-26	03-Dec-26	24-Oct-26 A	27-Oct-26	0.00	10,529.25	52,646.24	33
METAL WORKS		14	100%	0%	05-Oct-26	20-Oct-26	19-Nov-26	05-Dec-26	3,899.72	0.00	3,899.72	-39
MLTX-02-005-CN-129	Installation of DI Cover for Tank	14	100%	0%	05-Oct-26	20-Oct-26	19-Nov-26	05-Dec-26	3,899.72	0.00	3,899.72	-39
FINISHING WORKS		83	71%	41.06%	18-Oct-26	16-Dec-26	27-Sep-26 A	21-Jan-27	58,109.58	33,607.92	81,842.14	-31
FLOOR FINISHES		23	0%	0%	21-Nov-26	16-Dec-26	27-Dec-26	21-Jan-27	0.00	0.00	1,169.94	-31
MLTX-02-005-CN-1	Epoxy Coat on Concrete Floor	23	0%	0%	21-Nov-26	16-Dec-26	27-Dec-26	21-Jan-27	0.00	0.00	1,169.94	-31
WALL FINISHES		52	72.03%	41.66%	18-Oct-26	03-Nov-26	27-Sep-26 A	13-Dec-26	58,109.58	33,607.92	80,672.20	-34
MLTX-02-005-CN-1	Painting Finish Works for External Walls	3	100%	90%	18-Oct-26	20-Oct-26	27-Sep-26 A	29-Oct-26	35,825.58	32,243.02	35,825.58	-8
MLTX-02-005-CN-1	Phenolic Partitions for Toilets	7	71.43%	0%	21-Oct-26	28-Oct-26	06-Dec-26	13-Dec-26	22,284.00	0.00	31,197.60	-39
MLTX-02-005-CN-1	Glass Partitions including all accessories and doors	5	0%	10%	29-Oct-26	03-Nov-26	24-Oct-26 A	27-Oct-26	0.00	1,364.90	13,649.02	7
SPECIALTIES WORK		92	25%	20%	27-Sep-26	23-Dec-26	04-Oct-26 A	11-Jan-27	14,623.96	11,699.17	58,495.83	-16
MLTX-02-005-CN-127	Sanitary Fixtures and Accessories Works	3	100%	80%	27-Sep-26	29-Sep-26	04-Oct-26 A	29-Oct-26	14,623.96	11,699.17	14,623.96	-26
MLTX-02-005-CN-127	Installation of MODON Logo on the entrance	17	0%	0%	05-Dec-26	23-Dec-26	23-Dec-26	11-Jan-27	0.00	0.00	19,498.61	-16
MLTX-02-005-CN-131	Installation of Phenolic Locker	12	0%	0%	28-Nov-26	10-Dec-26	14-Dec-26	27-Dec-26	0.00	0.00	24,373.26	-14
TESTING & COMMISSIONING		45	0%	0%	08-Dec-26	02-Jan-27	16-Jan-27	09-Mar-27	0.00	0.00	0.00	-56
MLTX-02-005-TC-11890	Testing and Commissioning for MEP Works for Playground	18	0%	0%	12-Dec-26	31-Dec-26	16-Feb-27	09-Mar-27	0.00	0.00	0.00	-57
MLTX-02-005-TC-11900	Testing and Commissioning for MEP Works for Toilet/Service	7	0%	0%	26-Dec-26	02-Jan-27	01-Feb-27	08-Feb-27	0.00	0.00	0.00	-32
MLTX-02-005-TC-11910	Testing and Commissioning for MEP Works for Landscape	21	0%	0%	08-Dec-26	31-Dec-26	16-Jan-27	08-Feb-27	0.00	0.00	0.00	-33
DAMMAM		165	7.11%	4.45%	21-May-26	02-Jan-27	06-Sep-26 A	28-Feb-27	437,888.61	274,550.10	6,162,853.43	-48
ENGINEERING		50	0%	0%	25-May-26	02-Aug-26	27-Oct-26	23-Dec-26	0.00	0.00	0.00	-122

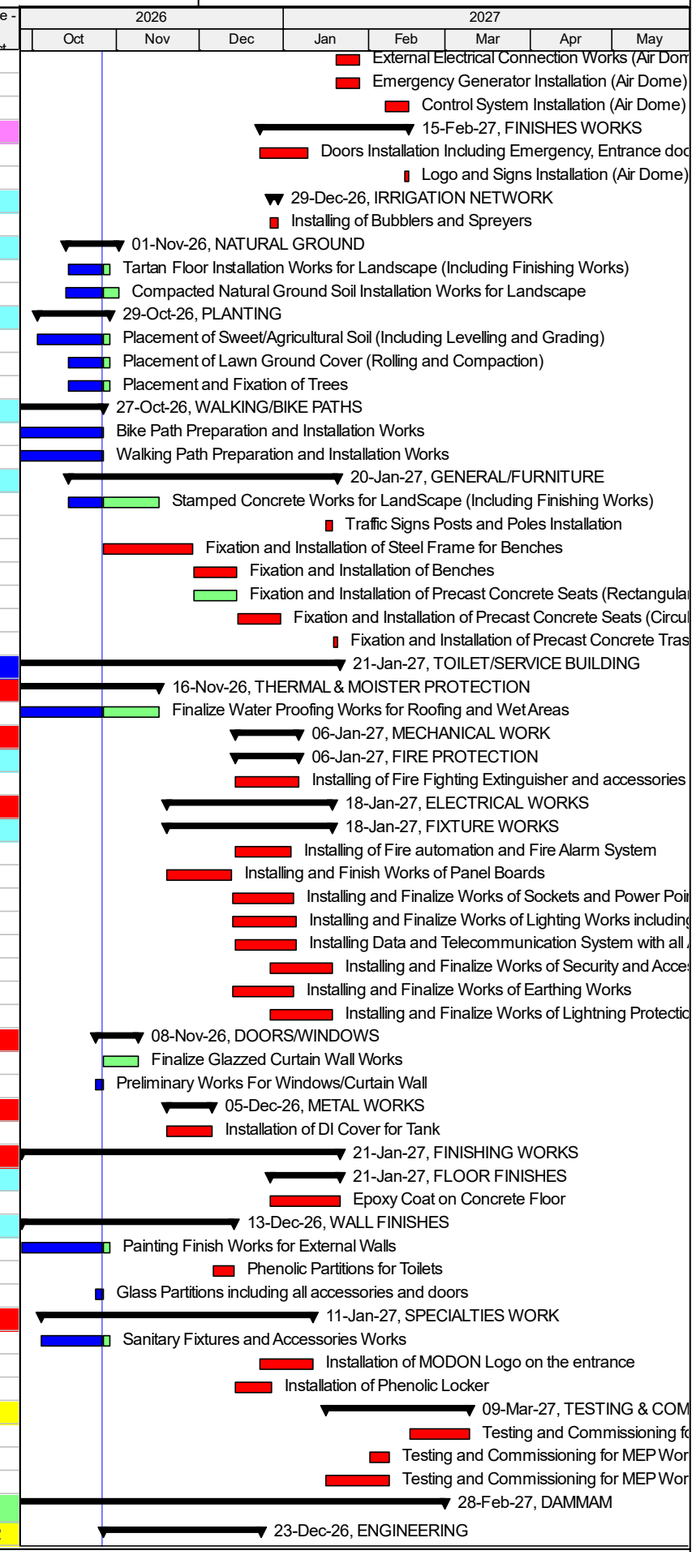

Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary

TASK filter: Remaining works.

© Oracle Corporation

MLTX-02-005 - Playground Initiative for Eastern Region (Arar-Hasa osis -Dammam)


Remaining work
D.D 26-10-2026

PROFAST شركة برو فاست المحدودة

egis

MODON مدن

Activity ID	Activity Name	Original Duration	Schedule % Complete	Performance % Complete	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Variance - BL Project
SHOP DRAWINGS		50	0%	0%	25-May-26	02-Aug-26	27-Oct-26	23-Dec-26	0.00	0.00	0.00	-122
SHOP DRAWINGS SUBMISSION		30	0%	0%	25-May-26	01-Jul-26	27-Oct-26	30-Nov-26	0.00	0.00	0.00	-129
SHOP DRAWINGS SUBMITTALS FOR PLAYGROUND WORKS		30	0%	0%	25-May-26	01-Jul-26	27-Oct-26	30-Nov-26	0.00	0.00	0.00	-129
ELECTRICAL WORKS		30	0%	0%	25-May-26	01-Jul-26	27-Oct-26	30-Nov-26	0.00	0.00	0.00	-129
MLTX-02-005-EI	Shop DWG Submittal for Power Layout	25	100%	0%	25-May-26	25-Jun-26	27-Oct-26	24-Nov-26	0.00	0.00	0.00	-129
MLTX-02-005-EI	Shop DWG Submittal for Power Installation Details	30	100%	0%	25-May-26	01-Jul-26	27-Oct-26	30-Nov-26	0.00	0.00	0.00	-129
SHOP DRAWINGS APPROVALS		25	0%	0%	02-Jul-26	02-Aug-26	25-Nov-26	23-Dec-26	0.00	0.00	0.00	-122
SHOP DRAWINGS APPROVAL FOR PLAYGROUND WORKS		25	0%	0%	02-Jul-26	02-Aug-26	25-Nov-26	23-Dec-26	0.00	0.00	0.00	-122
ELECTRICAL WORKS		25	0%	0%	02-Jul-26	02-Aug-26	25-Nov-26	23-Dec-26	0.00	0.00	0.00	-122
MLTX-02-005-EI	Shop DWG Approval for Power Layout	25	100%	0%	02-Jul-26	30-Jul-26	25-Nov-26	23-Dec-26	0.00	0.00	0.00	-124
MLTX-02-005-EI	Shop DWG Approval for Power Installation Details	15	100%	0%	16-Jul-26	02-Aug-26	01-Dec-26	17-Dec-26	0.00	0.00	0.00	-117
PROCUREMENT		91	0%	0%	21-May-26	21-Dec-26	27-Oct-26	09-Feb-27	0.00	0.00	0.00	-43
SHORT LEAD ITEM		91	0%	0%	21-May-26	21-Dec-26	27-Oct-26	09-Feb-27	0.00	0.00	0.00	-43
TOILET/SERVICE WORKS		41	0%	0%	17-Jun-26	28-Nov-26	27-Oct-26	13-Dec-26	0.00	0.00	0.00	-13
LIGHTING FIXTURES		10	0%	0%	22-Jul-26	02-Aug-26	30-Nov-26	10-Dec-26	0.00	0.00	0.00	-111
MLTX-02-005-PR-1	Material Delivery for Lighting Fixtures	10	100%	0%	22-Jul-26	02-Aug-26	30-Nov-26	10-Dec-26	0.00	0.00	0.00	-111
SWITCHES/SOCKETS		12	0%	0%	22-Jul-26	04-Aug-26	30-Nov-26	13-Dec-26	0.00	0.00	0.00	-111
MLTX-02-005-PR-1	PO for Switches/Sockets	5	100%	0%	22-Jul-26	27-Jul-26	30-Nov-26	05-Dec-26	0.00	0.00	0.00	-111
MLTX-02-005-PR-1	Material Delivery for Switches/Sockets	7	100%	0%	28-Jul-26	04-Aug-26	06-Dec-26	13-Dec-26	0.00	0.00	0.00	-111
DISTRIBUTION PANNELS		40	0%	0%	13-Oct-26	28-Nov-26	27-Oct-26	12-Dec-26	0.00	0.00	0.00	-12
MLTX-02-005-PR-1	PO for Distribution Panels	15	80%	0%	13-Oct-26	29-Oct-26	27-Oct-26	12-Nov-26	0.00	0.00	0.00	-12
MLTX-02-005-PR-1	Material Delivery for Distribution Panels	25	0%	0%	31-Oct-26	28-Nov-26	14-Nov-26	12-Dec-26	0.00	0.00	0.00	-12
FURNITURES		29	0%	0%	17-Jun-26	20-Jul-26	27-Oct-26	29-Nov-26	0.00	0.00	0.00	-112
MLTX-02-005-PR-1	PO for Furnitures	9	100%	0%	17-Jun-26	27-Jun-26	27-Oct-26	05-Nov-26	0.00	0.00	0.00	-112
MLTX-02-005-PR-1	Material Delivery for Furnitures	20	100%	0%	28-Jun-26	20-Jul-26	07-Nov-26	29-Nov-26	0.00	0.00	0.00	-112
PLAYGROUND WORKS		72	0%	0%	21-May-26	21-Dec-26	27-Oct-26	18-Jan-27	0.00	0.00	0.00	-24
PVC MEMBRANE		21	0%	0%	21-May-26	17-Jun-26	27-Oct-26	19-Nov-26	0.00	0.00	0.00	-132
MLTX-02-005-PR-1	Material Delivery for PVC Membrane	21	100%	0%	21-May-26	17-Jun-26	27-Oct-26	19-Nov-26	0.00	0.00	0.00	-132
ARTIFICIAL TURF		12	0%	0%	18-Jun-26	01-Jul-26	21-Nov-26	03-Dec-26	0.00	0.00	0.00	-132
MLTX-02-005-PR-1	Material Delivery for Artificial TURF	12	100%	0%	18-Jun-26	01-Jul-26	21-Nov-26	03-Dec-26	0.00	0.00	0.00	-132
RUBBER GRANULES		12	0%	0%	31-May-26	13-Jun-26	27-Oct-26	09-Nov-26	0.00	0.00	0.00	-127
MLTX-02-005-PR-1	Material Delivery for Rubber Granules	12	100%	0%	31-May-26	13-Jun-26	27-Oct-26	09-Nov-26	0.00	0.00	0.00	-127
PADEL GLASS		28	0%	0%	19-Oct-26	19-Nov-26	27-Oct-26	28-Nov-26	0.00	0.00	0.00	-7
MLTX-02-005-PR-1	Material Delivery for Padel Glass	28	25%	0%	19-Oct-26	19-Nov-26	27-Oct-26	28-Nov-26	0.00	0.00	0.00	-7
PADEL WIRE MESH/STEEL SETS		15	0%	0%	06-Jun-26	22-Jun-26	27-Oct-26	12-Nov-26	0.00	0.00	0.00	-122
MLTX-02-005-PR-1	Material Delivery for Wire Mesh/Steel Sets	15	100%	0%	06-Jun-26	22-Jun-26	27-Oct-26	12-Nov-26	0.00	0.00	0.00	-122
BITUMINOUS BASE & WEARING COURSE		32	0%	0%	15-Jun-26	21-Jul-26	27-Oct-26	02-Dec-26	0.00	0.00	0.00	-114
MLTX-02-005-PR-1	PO for Bituminous Base & Wearing Course	15	100%	0%	15-Jun-26	01-Jul-26	27-Oct-26	12-Nov-26	0.00	0.00	0.00	-114
MLTX-02-005-PR-1	Material Delivery for the Site	17	100%	0%	02-Jul-26	21-Jul-26	14-Nov-26	02-Dec-26	0.00	0.00	0.00	-114
MARKING PAINT		32	0%	0%	02-Jul-26	08-Aug-26	14-Nov-26	20-Dec-26	0.00	0.00	0.00	-114
MLTX-02-005-PR-1	PO for Marking Paint	15	100%	0%	02-Jul-26	19-Jul-26	14-Nov-26	30-Nov-26	0.00	0.00	0.00	-114
MLTX-02-005-PR-1	Material Delivery for Marking Paint	17	100%	0%	20-Jul-26	08-Aug-26	01-Dec-26	20-Dec-26	0.00	0.00	0.00	-114
POWER CABLES		15	0%	0%	29-Jun-26	15-Jul-26	27-Oct-26	12-Nov-26	0.00	0.00	0.00	-102
MLTX-02-005-PR-1	PO for Power Cables	5	100%	0%	29-Jun-26	04-Jul-26	27-Oct-26	01-Nov-26	0.00	0.00	0.00	-102
MLTX-02-005-PR-1	Material Delivery for Power Cables	10	100%	0%	05-Jul-26	15-Jul-26	02-Nov-26	12-Nov-26	0.00	0.00	0.00	-102
LIGHT FIXTURES		20	0%	0%	10-Nov-26	02-Dec-26	02-Nov-26	24-Nov-26	0.00	0.00	0.00	7
MLTX-02-005-PR-1	Material Delivery for Light Fixtures	20	0%	0%	10-Nov-26	02-Dec-26	02-Nov-26	24-Nov-26	0.00	0.00	0.00	7
CCTV MATERIALS		62	0%	0%	30-Jul-26	21-Dec-26	27-Oct-26	06-Jan-27	0.00	0.00	0.00	-14
MLTX-02-005-PR-1	PO for CCTV	5	100%	0%	30-Jul-26	04-Aug-26	27-Oct-26	01-Nov-26	0.00	0.00	0.00	-75
MLTX-02-005-PR-1	Material Delivery for CCTV	15	0%	0%	05-Dec-26	21-Dec-26	21-Dec-26	06-Jan-27	0.00	0.00	0.00	-14
POWER OUTLETS/SWITCHES		31	0%	0%	08-Aug-26	08-Dec-26	14-Dec-26	18-Jan-27	0.00	0.00	0.00	-35
MLTX-02-005-PR-1	PO for Power Outlets/Switches	6	100%	0%	08-Aug-26	13-Aug-26	14-Dec-26	20-Dec-26	0.00	0.00	0.00	-109
MLTX-02-005-PR-1	Material Delivery for Power Outlets/Switches	25	0%	0%	10-Nov-26	08-Dec-26	21-Dec-26	18-Jan-27	0.00	0.00	0.00	-35
LANDSCAPE WORKS		62	0%	0%	15-Aug-26	13-Dec-26	30-Nov-26	09-Feb-27	0.00	0.00	0.00	-50
PAVEMENT MARKING		15	0%	0%	15-Aug-26	31-Aug-26	21-Dec-26	06-Jan-27	0.00	0.00	0.00	-109
MLTX-02-005-PR-1	PO for Pavement Markings	5	100%	0%	15-Aug-26	19-Aug-26	21-Dec-26	26-Dec-26	0.00	0.00	0.00	-109
MLTX-02-005-PR-1	Material Delivery for Pavement Markings	10	100%	0%	20-Aug-26	31-Aug-26	27-Dec-26	06-Jan-27	0.00	0.00	0.00	-109
TRAFFIC SIGNS		19	0%	0%	22-Nov-26	13-Dec-26	19-Jan-27	09-Feb-27	0.00	0.00	0.00	-50
MLTX-02-005-PR-1	Material Delivery for Traffic Signs	19	0%	0%	22-Nov-26	13-Dec-26	19-Jan-27	09-Feb-27	0.00	0.00	0.00	-50
IRRIGATION PIPES/SPRINKLERS		8	0%	0%	22-Nov-26	30-Nov-26	30-Nov-26	08-Dec-26	0.00	0.00	0.00	-7
MLTX-02-005-PR-1	Material Delivery for Irrigation Pipes/Sprinkles	8	0%	0%	22-Nov-26	30-Nov-26	30-Nov-26	08-Dec-26	0.00	0.00	0.00	-7
TRACK SURFACE		10	0%	0%	10-Nov-26	21-Nov-26	07-Jan-27	18-Jan-27	0.00	0.00	0.00	-50
MLTX-02-005-PR-1	Material Delivery for Track Surface	10	0%	0%	10-Nov-26	21-Nov-26	07-Jan-27	18-Jan-27	0.00	0.00	0.00	-50
GRASS/TREES		15	0%	0%	22-Nov-26	08-Dec-26	19-Jan-27	04-Feb-27	0.00	0.00	0.00	-50

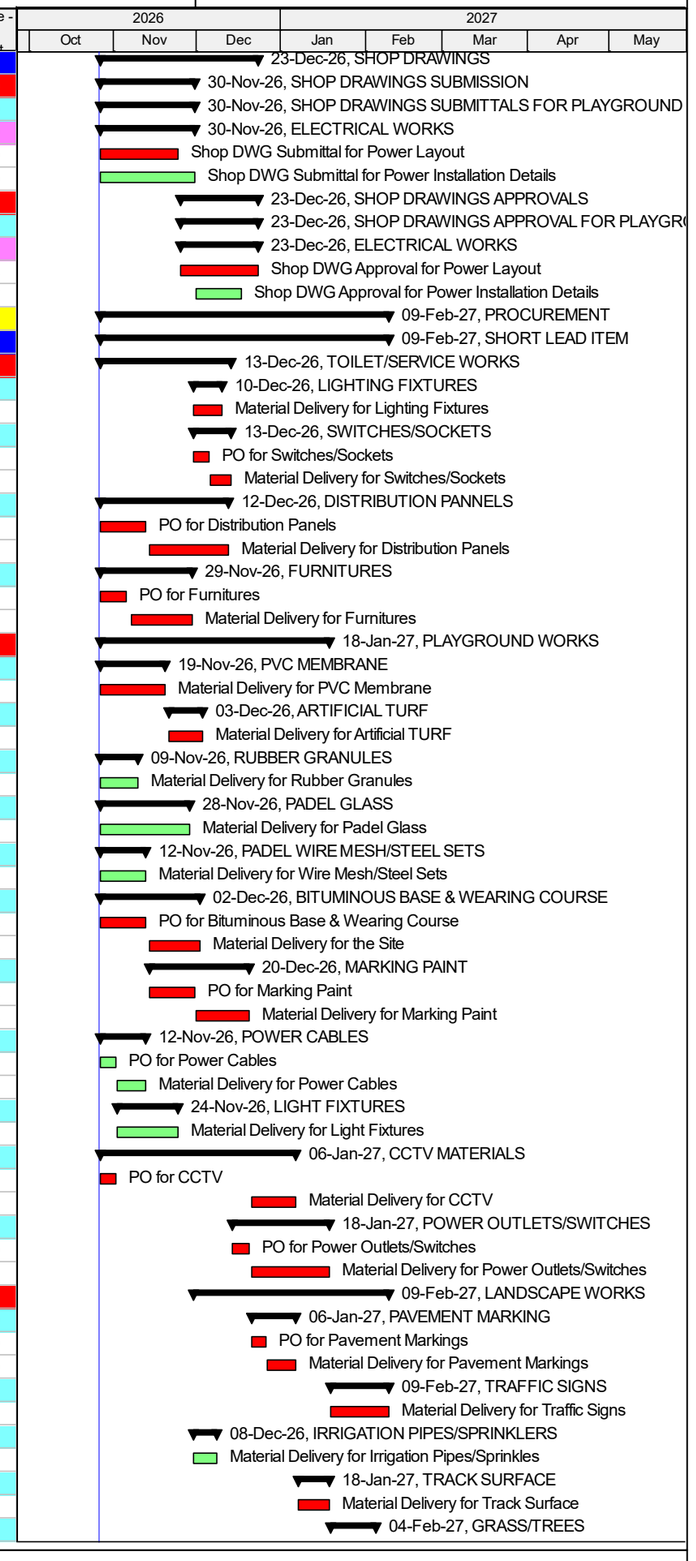

Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary

TASK filter: Remaining works.

© Oracle Corporation

MLTX-02-005 - Playground Initiative for Eastern Region (Arar-Hasa osis -Dammam)


Remaining work
D.D 26-10-2026

PROFAST شركة برو فاست المحدودة

egis

MODON مدن

Activity ID	Activity Name	Original Duration	Schedule % Complete	Performance % Complete	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Variance - BL Project
MLTX-02-005-PR-1	Material Delivery for Grass/Trees	15	0%	0%	22-Nov-26	08-Dec-26	19-Jan-27	04-Feb-27	0.00	0.00	0.00	-50
LONG LEAD ITEM		22	0%	0%	07-Sep-26	30-Nov-26	27-Oct-26	21-Nov-26	0.00	0.00	0.00	8
PLAYGROUND WORKS		22	0%	0%	07-Sep-26	30-Nov-26	27-Oct-26	21-Nov-26	0.00	0.00	0.00	8
STEEL TENSION CABLES		22	0%	0%	07-Sep-26	19-Oct-26	27-Oct-26	21-Nov-26	0.00	0.00	0.00	-28
MLTX-02-005-PR-1	Material Delivery for Steel Tension Cables	15	100%	0%	07-Sep-26	24-Sep-26	27-Oct-26	12-Nov-26	0.00	0.00	0.00	-42
MLTX-02-005-PR-1	Staging time	7	100%	0%	12-Oct-26	19-Oct-26	14-Nov-26	21-Nov-26	0.00	0.00	0.00	-28
EMERGENCY DOORS		18	0%	0%	04-Nov-26	24-Nov-26	27-Oct-26	16-Nov-26	0.00	0.00	0.00	7
MLTX-02-005-PR-1	Material Delivery for Emergency Doors	15	0%	0%	04-Nov-26	21-Nov-26	27-Oct-26	12-Nov-26	0.00	0.00	0.00	7
MLTX-02-005-PR-1	Staging time	3	0%	0%	22-Nov-26	24-Nov-26	14-Nov-26	16-Nov-26	0.00	0.00	0.00	7
PRESSURE UNITS		22	0%	0%	05-Nov-26	30-Nov-26	27-Oct-26	21-Nov-26	0.00	0.00	0.00	8
MLTX-02-005-PR-1	Material Delivery for Pressure Units	10	0%	0%	05-Nov-26	16-Nov-26	27-Oct-26	07-Nov-26	0.00	0.00	0.00	8
MLTX-02-005-PR-1	Staging time	10	0%	0%	19-Nov-26	30-Nov-26	10-Nov-26	21-Nov-26	0.00	0.00	0.00	8
AIR LOCK DOORS		20	0%	0%	05-Nov-26	26-Nov-26	27-Oct-26	18-Nov-26	0.00	0.00	0.00	7
MLTX-02-005-PR-1	Material Delivery for Lock Doors	12	0%	0%	05-Nov-26	18-Nov-26	27-Oct-26	09-Nov-26	0.00	0.00	0.00	8
MLTX-02-005-PR-1	Staging time	5	0%	0%	22-Nov-26	26-Nov-26	14-Nov-26	18-Nov-26	0.00	0.00	0.00	7
CONSTRUCTION PHASE		165	7.11%	4.45%	02-Jul-26	31-Dec-26	06-Sep-26 A	28-Feb-27	437,888.61	274,550.10	6,162,853.43	-49
SITE WORKS		111	7.11%	4.22%	02-Jul-26	31-Dec-26	15-Oct-26 A	28-Feb-27	417,381.61	247,904.38	5,868,751.92	-49
LANDSCAPE WORKS		111	7.11%	4.22%	02-Jul-26	31-Dec-26	15-Oct-26 A	28-Feb-27	417,381.61	247,904.38	5,868,751.92	-49
PLAYGROUND AREA		71	56.17%	5.98%	02-Jul-26	31-Dec-26	21-Oct-26 A	03-Feb-27	338,945.66	36,104.13	603,475.37	-29
FOOTBALL PLAYGROUND		43	76.92%	0%	02-Jul-26	15-Dec-26	05-Dec-26	23-Jan-27	158,424.99	0.00	205,952.49	-33
MLTX-02-005-CI	Finishing Asphalt & Concrete Surface (Football Playground)	20	100%	0%	02-Jul-26	25-Jul-26	05-Dec-26	27-Dec-26	158,424.99	0.00	158,424.99	-132
MLTX-02-005-CI	Install Sport Equipments - Goal / Nets - (Football Playground)	5	0%	0%	10-Dec-26	15-Dec-26	18-Jan-27	23-Jan-27	0.00	0.00	31,685.00	-33
MLTX-02-005-CI	Surface Marking and Painting (Football Playground)	2	0%	0%	08-Dec-26	09-Dec-26	16-Jan-27	17-Jan-27	0.00	0.00	15,842.50	-33
PADEL PLAYGROUND		5	0%	0%	20-Dec-26	24-Dec-26	27-Jan-27	01-Feb-27	0.00	0.00	70,195.20	-33
MLTX-02-005-CI	Install Sport Equipments - Goal / Nets - (Padel Playground)	5	0%	0%	20-Dec-26	24-Dec-26	27-Jan-27	01-Feb-27	0.00	0.00	58,496.00	-33
MLTX-02-005-CI	Surface Marking and Painting (Padel Playground)	5	0%	0%	20-Dec-26	24-Dec-26	27-Jan-27	01-Feb-27	0.00	0.00	11,699.20	-33
BASKETBALL PLAYGROUND		2	0%	0%	30-Dec-26	31-Dec-26	02-Feb-27	03-Feb-27	0.00	0.00	96,956.10	-29
MLTX-02-005-CI	Install Sport Equipments - Goal / Nets - (Basketball	2	0%	0%	30-Dec-26	31-Dec-26	02-Feb-27	03-Feb-27	0.00	0.00	80,796.75	-29
MLTX-02-005-CI	Surface Marking and Painting (Basketball Playground)	2	0%	0%	30-Dec-26	31-Dec-26	02-Feb-27	03-Feb-27	0.00	0.00	16,159.35	-29
PADEL FENCE		48	0%	0%	26-Nov-26	24-Dec-26	29-Nov-26	23-Jan-27	0.00	0.00	49,850.91	-25
MLTX-02-005-CI	Tempered Glass Fenc Installation and Fixation	25	0%	0%	26-Nov-26	24-Dec-26	29-Nov-26	27-Dec-26	0.00	0.00	30,677.48	-2
MLTX-02-005-CI	Chain Link Fence Installation and Fixation	25	0%	0%	26-Nov-26	24-Dec-26	29-Nov-26	27-Dec-26	0.00	0.00	15,338.75	-2
MLTX-02-005-CI	Install of Fence Gates	5	0%	0%	20-Dec-26	24-Dec-26	18-Jan-27	23-Jan-27	0.00	0.00	3,834.68	-25
CURBSTOEN/INTERLOCK		6	100%	20%	15-Sep-26	21-Sep-26	21-Oct-26 A	02-Nov-26	180,520.67	36,104.13	180,520.67	-35
MLTX-02-005-CI	Interlock Installation (Grey Scale) for LandScape (Including	6	100%	20%	15-Sep-26	21-Sep-26	21-Oct-26 A	02-Nov-26	180,520.67	36,104.13	180,520.67	-35
AIR DOME		30	0%	0%	15-Nov-26	24-Dec-26	23-Dec-26	26-Jan-27	0.00	0.00	4,306,367.09	-28
CIVIL WORKS		20	0%	0%	15-Nov-26	07-Dec-26	23-Dec-26	14-Jan-27	0.00	0.00	1,391,301.90	-33
MLTX-02-005-CI	Install of Membrane Covering System (Air Dome)	20	0%	0%	15-Nov-26	07-Dec-26	23-Dec-26	14-Jan-27	0.00	0.00	942,830.33	-33
MLTX-02-005-CI	Thermal Insulation Works (Air Dome)	20	0%	0%	15-Nov-26	07-Dec-26	23-Dec-26	14-Jan-27	0.00	0.00	448,471.57	-33
MECHANICAL WORKS		5	0%	0%	08-Dec-26	13-Dec-26	16-Jan-27	20-Jan-27	0.00	0.00	1,233,296.81	-33
MLTX-02-005-CI	Air Ducts and Grills Installation (Air Dome)	4	0%	0%	08-Dec-26	12-Dec-26	16-Jan-27	19-Jan-27	0.00	0.00	728,766.30	-33
MLTX-02-005-CI	Air Units Installation (Air Dome)	5	0%	0%	08-Dec-26	13-Dec-26	16-Jan-27	20-Jan-27	0.00	0.00	336,353.67	-33
MLTX-02-005-CI	Exhaust Fans and Ducts Installation (Air Dome)	5	0%	0%	08-Dec-26	13-Dec-26	16-Jan-27	20-Jan-27	0.00	0.00	168,176.84	-33
ELECTRICAL WORKS		10	0%	0%	08-Dec-26	24-Dec-26	16-Jan-27	26-Jan-27	0.00	0.00	1,513,591.54	-28
MLTX-02-005-CI	Light Fixture Works (Air Dome)	10	0%	0%	08-Dec-26	19-Dec-26	16-Jan-27	26-Jan-27	0.00	0.00	224,235.78	-33
MLTX-02-005-CI	Distribution Board and Electrical Works (Air Dome)	7	0%	0%	12-Dec-26	19-Dec-26	19-Jan-27	26-Jan-27	0.00	0.00	168,176.84	-33
MLTX-02-005-CI	External Electrical Connection Works (Air Dome)	6	0%	0%	13-Dec-26	19-Dec-26	20-Jan-27	26-Jan-27	0.00	0.00	168,176.84	-33
MLTX-02-005-CI	Emergency Generator Installation (Air Dome)	4	0%	0%	15-Dec-26	19-Dec-26	23-Jan-27	26-Jan-27	0.00	0.00	504,530.51	-33
MLTX-02-005-CI	Control System Installation (Air Dome)	3	0%	0%	22-Dec-26	24-Dec-26	24-Jan-27	26-Jan-27	0.00	0.00	448,471.57	-28
FINISHES WORKS		4	0%	0%	12-Dec-26	15-Dec-26	19-Jan-27	23-Jan-27	0.00	0.00	168,176.84	-33
MLTX-02-005-CI	Doors Installation Including Emergency, Entrance doors (Air	2	0%	0%	12-Dec-26	13-Dec-26	19-Jan-27	20-Jan-27	0.00	0.00	112,117.89	-33
MLTX-02-005-CI	Logo and Signs Installation (Air Dome)	2	0%	0%	14-Dec-26	15-Dec-26	21-Jan-27	23-Jan-27	0.00	0.00	56,058.95	-33
IRRIGATION NETWORK		2	0%	0%	01-Dec-26	02-Dec-26	30-Jan-27	31-Jan-27	0.00	0.00	25,106.20	-51
MLTX-02-005-CN-1	Installing of Bubblers and Spreyers	2	0%	0%	01-Dec-26	02-Dec-26	30-Jan-27	31-Jan-27	0.00	0.00	25,106.20	-51
NATURAL GROUND		35	33.9%	16.95%	10-Oct-26	12-Nov-26	20-Oct-26 A	30-Nov-26	65,000.00	32,500.00	191,740.00	-15
MLTX-02-005-CN-1	Tartan Floor Installation Works for Landscape (Including	15	0%	0%	27-Oct-26	12-Nov-26	14-Nov-26	30-Nov-26	0.00	0.00	126,740.00	-15
MLTX-02-005-CN-1	Compacted Natural Ground Soil Installation Works for	15	100%	50%	10-Oct-26	26-Oct-26	20-Oct-26 A	12-Nov-26	65,000.00	32,500.00	65,000.00	-15
PLANTING		23	0%	6%	06-Dec-26	31-Dec-26	24-Oct-26 A	25-Feb-27	0.00	20,835.09	347,251.46	-47
MLTX-02-005-CN-1	Placement of Sweet/Agricultural Soil (Including Levelling and	6	0%	20%	06-Dec-26	12-Dec-26	24-Oct-26 A	02-Nov-26	0.00	20,835.09	104,175.44	34
MLTX-02-005-CN-1	Placement of Lawn Ground Cover (Rolling and Compaction)	7	0%	0%	24-Dec-26	31-Dec-26	17-Feb-27	25-Feb-27	0.00	0.00	141,732.50	-47
MLTX-02-005-CN-1	Placement and Fixation of Trees	10	0%	0%	13-Dec-26	23-Dec-26	06-Feb-27	16-Feb-27	0.00	0.00	101,343.52	-47
GENERAL/FURNITURE		81	3.4%	40.14%	11-Oct-26	31-Dec-26	15-Oct-26 A	28-Feb-27	13,435.95	158,465.16	394,811.80	-49
MLTX-02-005-CN-1	Stamped Concrete Works for LandScape (Including	18	0%	0%	01-Nov-26	21-Nov-26	16-Dec-26	05-Jan-27	0.00	0.00	93,594.00	-39
MLTX-02-005-CN-1	Traffic Signs Posts and Poles Installation	15	0%	0%	15-Dec-26	31-Dec-26	10-Feb-27	28-Feb-27	0.00	0.00	9,749.30	-49

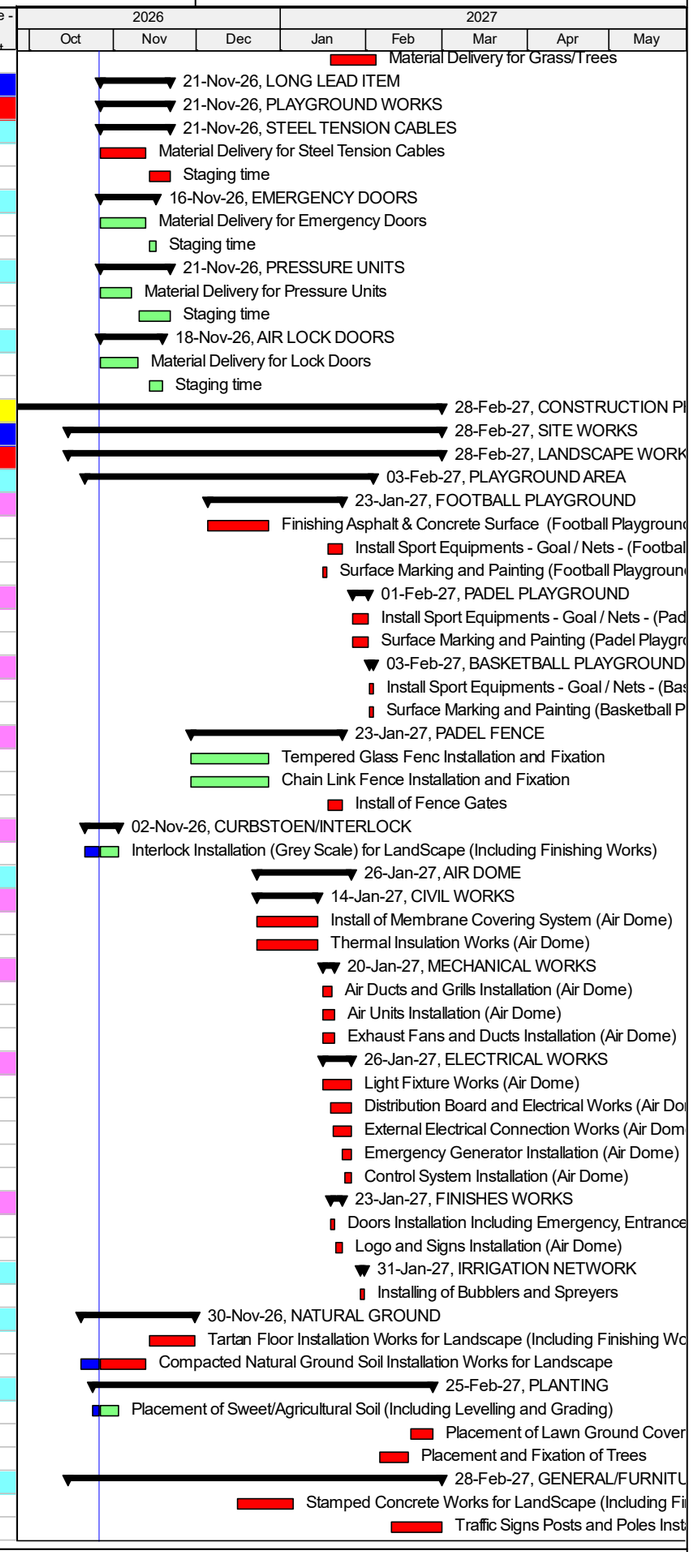

Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary


TASK filter: Remaining works.

© Oracle Corporation

MLTX-02-005 - Playground Initiative for Eastern Region (Arar-Hasa osis -Dammam)

Remaining work
D.D 26-10-2026

Activity ID	Activity Name	Original Duration	Schedule % Complete	Performance % Complete	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Variance - BL Project
MLTX-02-005-CN-1	Fixation and Installation of Steel Frame for Benches	18	77.78%	0%	11-Oct-26	31-Oct-26	25-Nov-26	15-Dec-26	13,435.95	0.00	17,274.79	-39
MLTX-02-005-CN-1	Fixation and Installation of Benches	20	0%	0%	01-Nov-26	23-Nov-26	06-Jan-27	28-Jan-27	0.00	0.00	40,307.84	-57
MLTX-02-005-CN-1	Fixation and Installation of Precast Concrete Seats	20	0%	0%	01-Nov-26	23-Nov-26	06-Jan-27	28-Jan-27	0.00	0.00	32,757.76	-57
MLTX-02-005-CN-1	Fixation and Installation of Precast Concrete Seats (Circular)	20	0%	0%	01-Nov-26	23-Nov-26	06-Jan-27	28-Jan-27	0.00	0.00	12,869.04	-57
MLTX-02-005-CN-1	Fixation and Installation of Precast Concrete Trash Bins	18	0%	0%	24-Nov-26	14-Dec-26	30-Jan-27	18-Feb-27	0.00	0.00	12,186.67	-57
MLTX-02-005-CN-1	Installing of Site Light Poles	20	0%	90%	22-Nov-26	14-Dec-26	15-Oct-26 A	18-Nov-26	0.00	158,465.16	176,072.40	22
TOILET/SERVICE BUILDING		161	6.97%	9.06%	18-Aug-26	29-Dec-26	06-Sep-26 A	23-Feb-27	20,507.00	26,645.72	294,101.51	-47
THERMAL & MOISTER PROTECTION		8	100%	90%	18-Aug-26	26-Aug-26	06-Sep-26 A	04-Nov-26	16,607.28	14,946.55	16,607.28	-59
MLTX-02-005-CN-140	Finalize Water Proofing Works for Roofing and Wet Areas	8	100%	90%	18-Aug-26	26-Aug-26	06-Sep-26 A	04-Nov-26	16,607.28	14,946.55	16,607.28	-59
MECHANICAL WORK		12	0%	0%	13-Dec-26	26-Dec-26	27-Dec-26	09-Jan-27	0.00	0.00	1,949.87	-12
FIRE PROTECTION		12	0%	0%	13-Dec-26	26-Dec-26	27-Dec-26	09-Jan-27	0.00	0.00	1,949.87	-12
MLTX-02-005-CN-1	Installing of Fire Fighting Extinguisher and accessories	12	0%	0%	13-Dec-26	26-Dec-26	27-Dec-26	09-Jan-27	0.00	0.00	1,949.87	-12
ELECTRICAL WORKS		57	0%	0%	23-Nov-26	29-Dec-26	17-Nov-26	21-Jan-27	0.00	0.00	180,781.27	-20
FIXTURE WORKS		57	0%	0%	23-Nov-26	29-Dec-26	17-Nov-26	21-Jan-27	0.00	0.00	180,781.27	-20
MLTX-02-005-CN-1	Installing of Fire automation and Fire Alarm System	15	0%	0%	12-Dec-26	28-Dec-26	27-Dec-26	12-Jan-27	0.00	0.00	34,317.53	-13
MLTX-02-005-CN-1	Installing and Finish Works of Panel Boards	21	0%	0%	06-Dec-26	29-Dec-26	27-Dec-26	19-Jan-27	0.00	0.00	102,367.69	-18
MLTX-02-005-CN-1	Installing and Finalize Works of Sockets and Power Points	13	0%	0%	12-Dec-26	26-Dec-26	27-Dec-26	10-Jan-27	0.00	0.00	7,085.10	-13
MLTX-02-005-CN-1	Installing and Finalize Works of Lighting Works including Light	14	0%	0%	12-Dec-26	27-Dec-26	27-Dec-26	11-Jan-27	0.00	0.00	14,259.43	-13
MLTX-02-005-CN-1	Installing Data and Telecommunication System with all	14	0%	0%	12-Dec-26	27-Dec-26	27-Dec-26	11-Jan-27	0.00	0.00	6,239.59	-13
MLTX-02-005-CN-1	Installing and Finalize Works of Security and Access Control	14	0%	0%	25-Nov-26	10-Dec-26	17-Nov-26	02-Dec-26	0.00	0.00	7,250.09	7
MLTX-02-005-CN-1	Installing and Finalize Works of Earthing Works	23	0%	0%	23-Nov-26	19-Dec-26	27-Dec-26	21-Jan-27	0.00	0.00	6,824.51	-29
MLTX-02-005-CN-1	Installing and Finalize Works of Lightning Protection System	15	0%	0%	13-Dec-26	29-Dec-26	03-Dec-26	20-Dec-26	0.00	0.00	2,437.33	8
METAL WORKS		14	100%	0%	11-Oct-26	26-Oct-26	25-Nov-26	10-Dec-26	3,899.72	0.00	3,899.72	-39
MLTX-02-005-CN-142	Installation of DI Cover for Tank	14	100%	0%	11-Oct-26	26-Oct-26	25-Nov-26	10-Dec-26	3,899.72	0.00	3,899.72	-39
FINISHING WORKS		27	0%	0%	01-Nov-26	21-Dec-26	12-Dec-26	11-Jan-27	0.00	0.00	32,367.54	-18
FLOOR FINISHES		14	0%	0%	06-Dec-26	21-Dec-26	27-Dec-26	11-Jan-27	0.00	0.00	1,169.94	-18
MLTX-02-005-CN-1	Epoxy Coat on Concrete Floor	14	0%	0%	06-Dec-26	21-Dec-26	27-Dec-26	11-Jan-27	0.00	0.00	1,169.94	-18
WALL FINISHES		11	0%	0%	01-Nov-26	12-Nov-26	12-Dec-26	23-Dec-26	0.00	0.00	31,197.60	-35
MLTX-02-005-CN-1	Phenolic Partitions for Toilets	11	0%	0%	01-Nov-26	12-Nov-26	12-Dec-26	23-Dec-26	0.00	0.00	31,197.60	-35
SPECIALTIES WORK		52	0%	20%	27-Oct-26	23-Dec-26	12-Oct-26 A	23-Feb-27	0.00	11,699.17	58,495.83	-52
MLTX-02-005-CN-141	Sanitary Fixtures and Accessories Works	4	0%	80%	27-Oct-26	31-Oct-26	12-Oct-26 A	10-Dec-26	0.00	11,699.17	14,623.96	-35
MLTX-02-005-CN-141	Installation of MODON Logo on the entrance	15	0%	0%	07-Dec-26	23-Dec-26	06-Feb-27	23-Feb-27	0.00	0.00	19,498.61	-52
MLTX-02-005-CN-145	Installation of Phenolic Locker	2	0%	0%	14-Nov-26	15-Nov-26	24-Dec-26	26-Dec-26	0.00	0.00	24,373.26	-35
TESTING & COMMISSIONING		7	0%	0%	24-Dec-26	02-Jan-27	20-Feb-27	28-Feb-27	0.00	0.00	0.00	-48
MLTX-02-005-TC-11920	Testing and Commissioning for MEP Works for Playground	5	0%	0%	27-Dec-26	31-Dec-26	23-Feb-27	28-Feb-27	0.00	0.00	0.00	-49
MLTX-02-005-TC-11930	Testing and Commissioning for MEP Works for Toilet/Service	3	0%	0%	30-Dec-26	02-Jan-27	25-Feb-27	28-Feb-27	0.00	0.00	0.00	-48
MLTX-02-005-TC-11940	Testing and Commissioning for MEP Works for Landscape	7	0%	0%	24-Dec-26	31-Dec-26	20-Feb-27	28-Feb-27	0.00	0.00	0.00	-49
PROJECT CLOSEOUT & DEMOBILIZATION		46	0%	0%	08-Dec-26	02-Jan-27	16-Jan-27	14-Mar-27	0.00	0.00	0.00	-57
As-Built DWGs		42	0%	0%	08-Dec-26	31-Dec-26	16-Jan-27	06-Mar-27	0.00	0.00	0.00	-54
As-Built DWGs Submittals		29	0%	0%	08-Dec-26	27-Dec-26	16-Jan-27	17-Feb-27	0.00	0.00	0.00	-45
MLTX-02-005-CO-1200(	As-Built DWGs Submittal for Playground Area Works	2	0%	0%	12-Dec-26	13-Dec-26	16-Feb-27	17-Feb-27	0.00	0.00	0.00	-57
MLTX-02-005-CO-1201(	As-Built DWGs Submittal for Toilet/Service Building Works	2	0%	0%	26-Dec-26	27-Dec-26	01-Feb-27	02-Feb-27	0.00	0.00	0.00	-32
MLTX-02-005-CO-1202(	As-Built DWGs Submittal for Landscape Works	4	0%	0%	08-Dec-26	12-Dec-26	16-Jan-27	19-Jan-27	0.00	0.00	0.00	-33
As-Built DWGs Approvals		38	0%	0%	15-Dec-26	31-Dec-26	20-Jan-27	06-Mar-27	0.00	0.00	0.00	-54
MLTX-02-005-CO-1204(	As-Built DWGs Approval for Playground Area Works	3	0%	0%	19-Dec-26	21-Dec-26	18-Feb-27	21-Feb-27	0.00	0.00	0.00	-53
MLTX-02-005-CO-1205(	As-Built DWGs Approval for Toilet/Service Building Works	3	0%	0%	29-Dec-26	31-Dec-26	03-Mar-27	06-Mar-27	0.00	0.00	0.00	-54
MLTX-02-005-CO-1206(	As-Built DWGs Approval for Landscape Works	3	0%	0%	15-Dec-26	17-Dec-26	20-Jan-27	23-Jan-27	0.00	0.00	0.00	-31
Demobilization		8	0%	0%	28-Dec-26	02-Jan-27	02-Mar-27	14-Mar-27	0.00	0.00	0.00	-57
MLTX-02-005-CO-12080	Demobilization of Manpower	1	0%	0%	28-Dec-26	28-Dec-26	02-Mar-27	02-Mar-27	0.00	0.00	0.00	-54
MLTX-02-005-CO-12090	Removal of Equipment from Site	1	0%	0%	28-Dec-26	28-Dec-26	02-Mar-27	02-Mar-27	0.00	0.00	0.00	-54
MLTX-02-005-CO-12100	Site Clean Up	1	0%	0%	31-Dec-26	31-Dec-26	03-Mar-27	03-Mar-27	0.00	0.00	0.00	-52
MLTX-02-005-CO-12110	Restoration of Ground Surfaces	1	0%	0%	02-Jan-27	02-Jan-27	14-Mar-27	14-Mar-27	0.00	0.00	0.00	-57

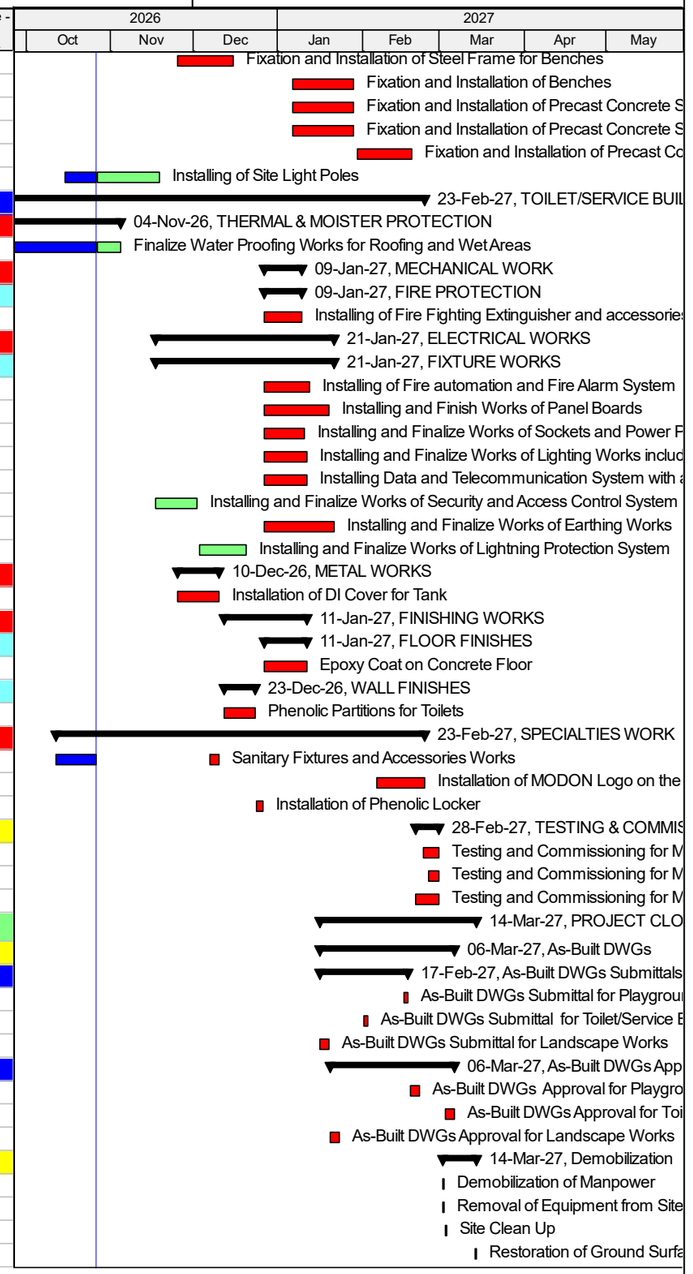

Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary

TASK filter: Remaining works.

© Oracle Corporation
