Infrastructure Networks for the 1 km² Logistics Zone, 2nd Industrial City, Dammam

شبكات البنية التحتية للمنطقة اللوجستية لمساحة 1 كم مربع بالمدينة الصناعية الثانية بالدمام

CLIENT	CONTRACTOR	CONSULTANT	MODON PM	SITE HANDOVER	CONTRACT COMPLETION
MODON	Shibh Aljazira Contracting Company	Egis	Muhammad H Al-Essa	30-Jul-2025	29-Jan-2027

Scope: phase 1 of the logistics area. Wet networks (sewerage, storm, potable water, fire fighting and TSE, including the force main), dry networks (medium voltage, low voltage, street lighting and telecom), the potable water pump station, the sewage lift station, guard rooms, all road layers up to the asphalt wearing course, and landscape.

Status at a glance

Progress is measured as physical % complete, weighted by budgeted man-hours. At the 20-Oct-2026 data date the project is 57.9% complete against 71.1% planned, 13.2% behind the plan (SPI 0.81). It gained 2.1% this week against 5.5% planned, so the gap widened from 9.7% to 13.2%.

PHYSICAL % COMPLETE

57.9% / 71.1% plan

▼ SPI 0.81 −13.2%

PROGRESS THIS WEEK

+2.1% / +5.5% plan

▼ 3.5% below the weekly plan

CONTRACT TIME ELAPSED

81.6% · day 447 of 548

▼ Forecast handover 01-Mar-2027

INVOICED TO DATE (GROSS)

31.6% · 62.9M SAR

7 invoices, last period ends 15-Sep-2026

With 81.6% of the contract time gone, 42.1% of the work remains.

Finishing by the contract completion date of 29-Jan-2027 needs about 2.9% a week, against 2.1% achieved this week. The revised plan reaches 92.9% by the end of November and 100% in December 2026. The weekly report's milestone sheet and the P6 update forecast project handover on 01-Mar-2027, 31 days late; the General Information sheet gives 14-Feb-2027. Construction is the weak phase: 45.1% done against 70.9% planned.

Site photos this week

Six site photos uploaded with the 20-Oct-2026 weekly report, camera-stamped 15 to 18 Oct 2026 where the stamp is visible. Asphalt, subgrade testing, duct works and the building works are shown. Select a photo to view it larger, then use the arrows to move between photos.



Asphalt paving

Paver and tandem roller on a new asphalt lane. No date stamp.



Field density test

Testing a compacted road layer. Camera-stamped 17-Oct-2026, 15:39, Dammam.



Duct laying in trench

Ducts set on timber spacers. Camera-stamped 15-Oct-2026, 09:09, Dammam.



Concrete in trench

Cast concrete strip along the trench. Camera-stamped 17-Oct-2026, 08:01, Dammam.



Building blockwork

Block walls rising between column starter bars. No date stamp.




Footing works

Concrete placing between column cages. Camera-stamped 18-Oct-2026, 06:49.

Progress S-curve

Cumulative physical progress (man-hour weighted), month-end values. Source: Physical-Chart Data sheet. The October actual is the 20-Oct value.

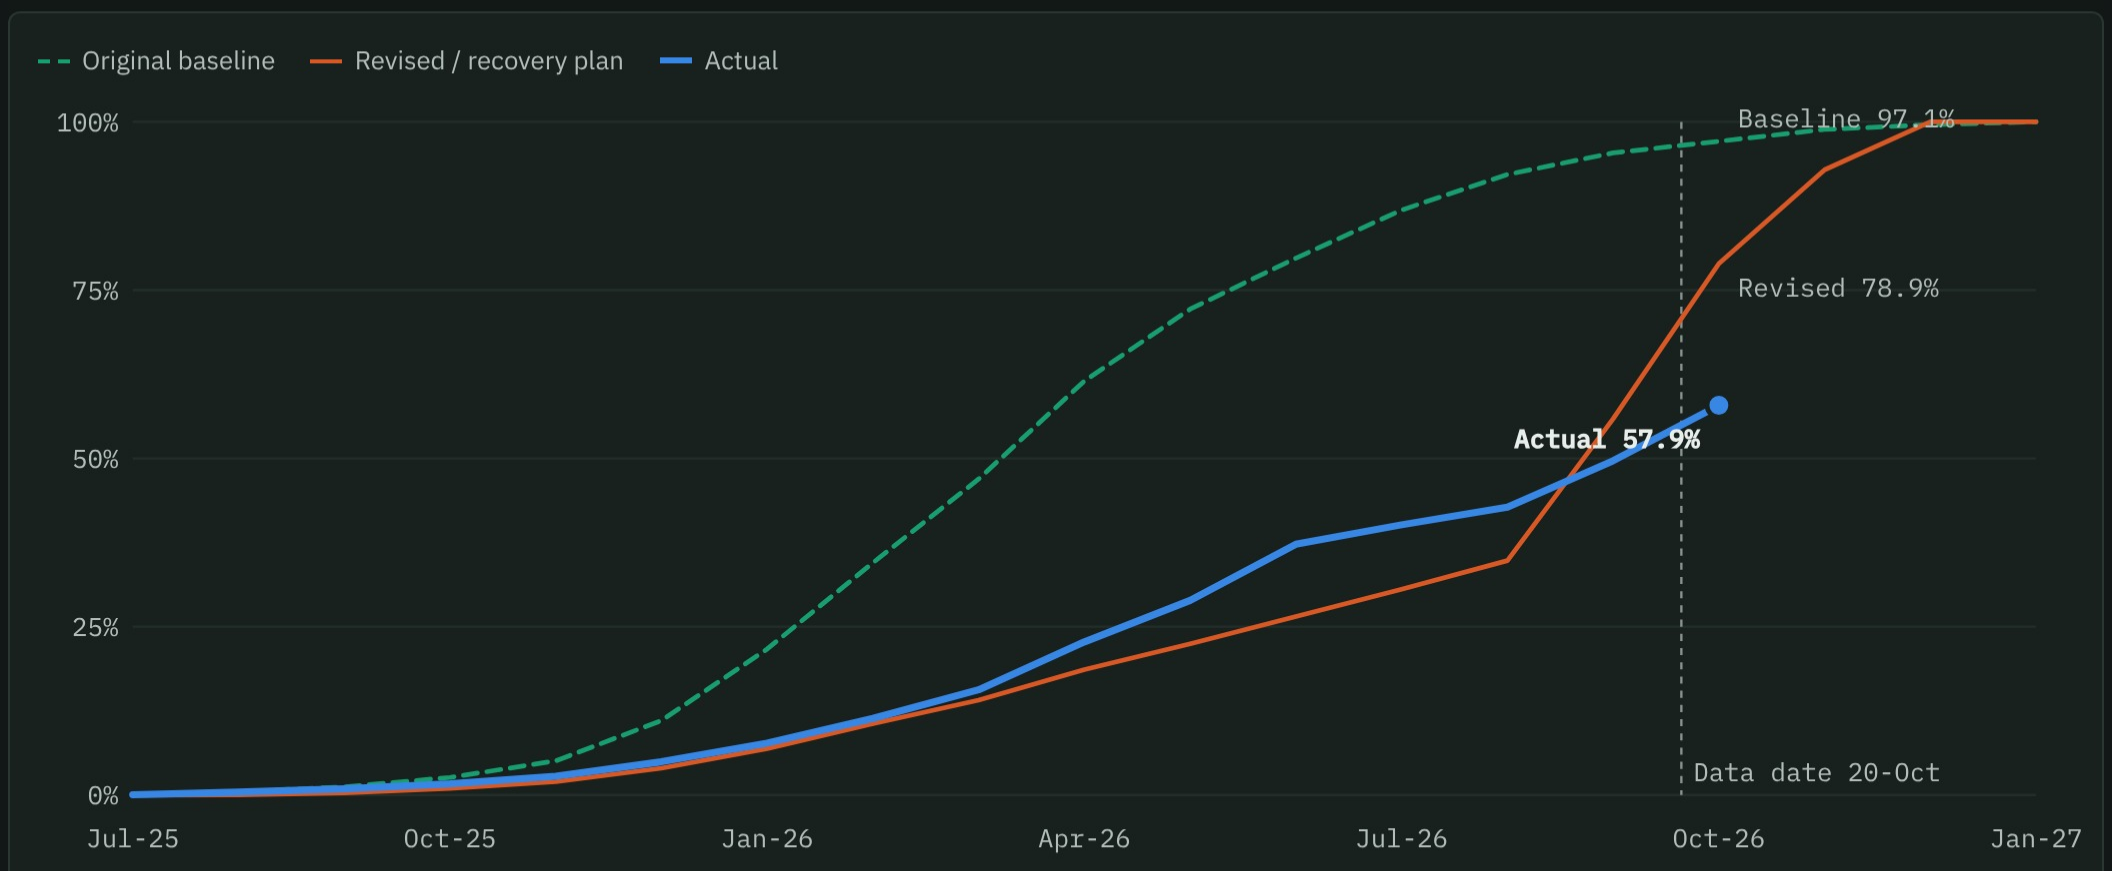

WEEK ENDING	PLANNED %	ACTUAL %	VARIANCE	GAINED THIS WEEK	SPI
13-Oct-2026*	65.6	55.8	−9.7	—	0.85
20-Oct-2026	**71.1**	**57.9**	**−13.2**	**+2.1**	**0.81**

* Only the latest weekly report was used. The 13-Oct row is derived from it: to-date values minus this week's values (planned +5.53%, actual +2.07%). Earlier weeks are not shown. The contractor's forecast in the same sheet reaches 79.4% by the end of November and 100% in January 2027.

Progress by phase

Physical progress to date by phase, weighted by budgeted man-hours, summed over all networks from the Progress sheet.


PHASE	WEIGHT	PLANNED	ACTUAL	VARIANCE	SPI	STATUS
Demolition & earthworks	2.9%	100.0%	96.7%	-3.3	0.97	▼ Slightly behind
Engineering	3.0%	100.0%	97.3%	-2.7	0.97	▼ Slightly behind
Procurement	27.0%	91.5%	92.7%	+1.2	1.01	▲ On track
Construction	57.1%	70.9%	45.1%	-25.8	0.64	▼ Behind
Testing & commissioning	10.0%	0.0%	14.1%	+14.1	–	▲ Started early
Total	100%	**71.1%**	**57.9%**	**-13.2**	**0.81**	▼ Behind

NETWORK / WORK PACKAGE	WEIGHT	PLANNED	ACTUAL	VARIANCE	SPI	STATUS
Demolition & site clearing	0.4%	100.0%	100.0%	0.0	1.00	✓ Complete
Earthworks & site grading	2.5%	100.0%	96.2%	-3.8	0.96	▼ Slightly behind
Sewerage network	8.1%	86.0%	82.9%	-3.1	0.96	▼ Slightly behind
Storm water network	15.6%	87.9%	82.5%	-5.5	0.94	▼ Slightly behind
Potable water network	6.3%	78.2%	59.7%	-18.5	0.76	▼ Behind
Fire fighting network	6.9%	74.1%	55.8%	-18.3	0.75	▼ Behind
TSE network	5.2%	63.2%	45.2%	-17.9	0.72	▼ Behind
Potable water pump station	7.8%	76.9%	68.0%	-8.9	0.88	▼ Behind
Sewage lift station	7.7%	84.0%	70.0%	-14.1	0.83	▼ Behind
Medium-voltage network	3.7%	68.7%	46.9%	-21.8	0.68	▼ Behind
Low-voltage network	3.4%	57.3%	35.5%	-21.9	0.62	▼ Behind
Street lighting network	8.3%	48.3%	33.5%	-14.8	0.69	▼ Behind
Telecom network	6.8%	59.2%	27.1%	-32.1	0.46	▼ Behind
Road works	8.7%	58.1%	34.4%	-23.7	0.59	▼ Behind
Landscape	4.9%	19.7%	31.6%	+11.8	1.60	▲ Ahead
Guard rooms	3.7%	85.9%	75.5%	-10.4	0.88	▼ Behind
Total	100%	**71.1%**	**57.9%**	**-13.2**	**0.81**	▼ Behind

Weights are budgeted man-hours. By contract value, road works is 39.8% of the contract and has earned 52.7% of its value against 65.8% planned. The P6 update (data date 20-Oct-2026) has 4,851 activities: 2,482 completed, 431 in progress and 1,938 not started. Failed-start activities rose from 993 to 1,047 this week.

Scope of work: quantities

Total, finished and remaining quantity for the main items, from the Major Quantities sheet of the 20-Oct-2026 weekly report. The sheet gives whole-site totals only, with no zones and no backfill figures. "This week" is shown as "—" because the latest report does not give the previous week's quantities.

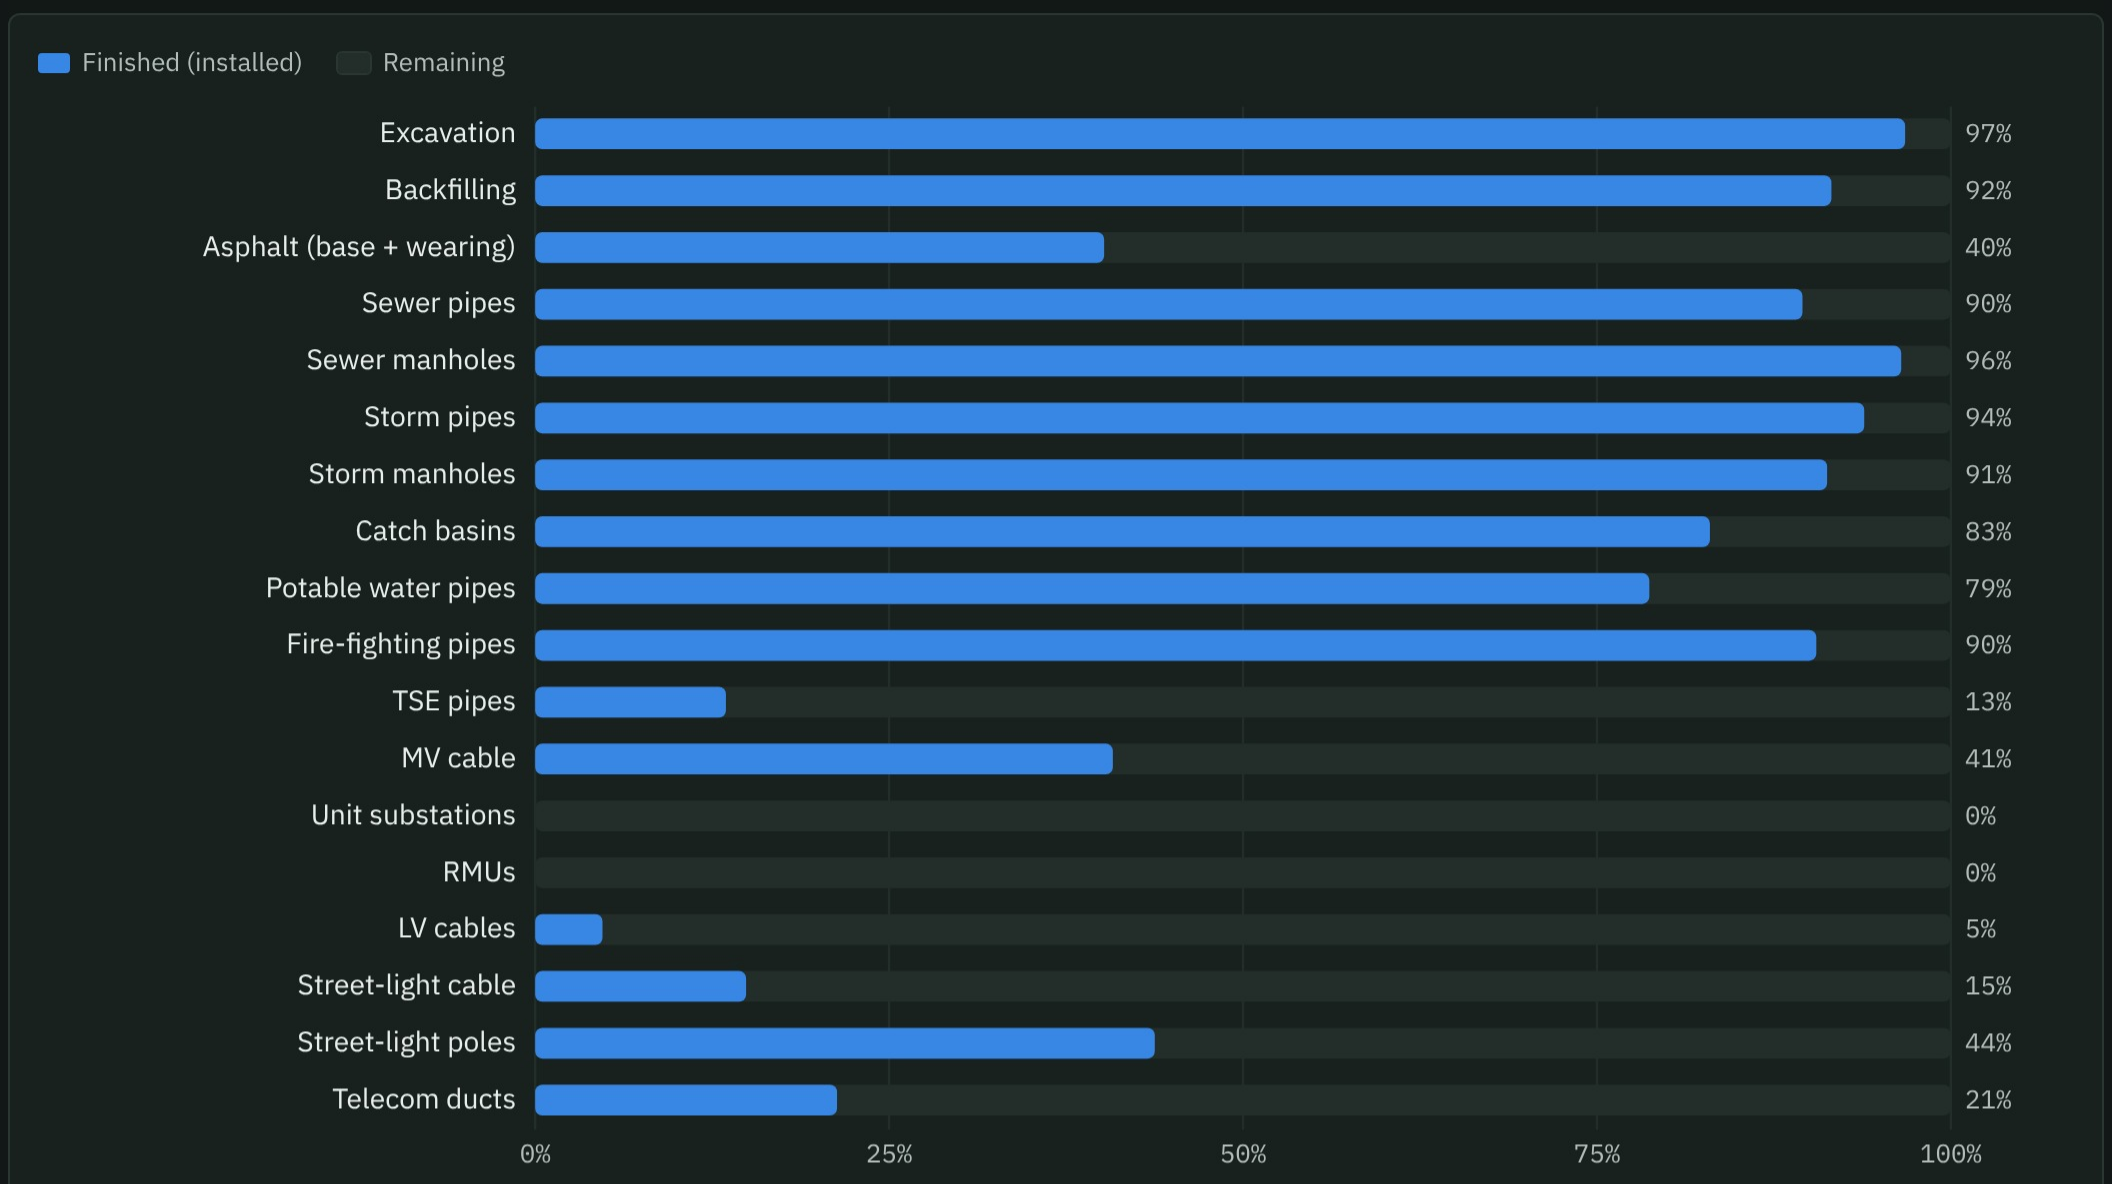

SCOPE ITEM	ZONE	UNIT	TOTAL	FINISHED	THIS WEEK	REMAINING	% FINISHED	BACKFILLED
Excavation	All	m³	853,395	825,821	–	27,574	96.8%	–
Backfilling	All	m³	1,481,028	1,356,040	–	124,988	91.6%	–
Asphalt (base + wearing)	All	m³	64,334	25,856	–	38,478	40.2%	–
Sewer pipes	All	LM	7,567	6,774	–	793.3	89.5%	–
Sewer manholes	All	EA	136	131.2	–	4.8	96.5%	–
Storm pipes	All	LM	14,821	13,914	–	907.2	93.9%	–
Storm manholes	All	EA	160	146	–	14	91.3%	–
Catch basins	All	EA	338	280.5	–	57.5	83.0%	–
Potable water pipes	All	LM	7,214	5,677	–	1,537	78.7%	–
Fire-fighting pipes	All	LM	6,355	5,751	–	604	90.5%	–
TSE pipes	All	LM	57,419	7,737	–	49,682	13.5%	–
MV cable	All	LM	12,559	5,125	–	7,434	40.8%	–
Unit substations	All	EA	3	0	–	3	0.0%	–
RMUs	All	EA	3	0	–	3	0.0%	–
LV cables	All	LM	14,370	683.4	–	13,687	4.8%	–
Street-light cable	All	LM	21,525	3,207	–	18,318	14.9%	–
Street-light poles	All	EA	565	247.3	–	317.7	43.8%	–
Telecom ducts	All	LM	11,057	2,358	–	8,699	21.3%	–

Wet networks mostly installed

Storm pipes are 93.9% installed, sewer pipes 89.5%, fire-fighting pipes 90.5% and potable water pipes 78.7%. Excavation is 96.8% and backfilling 91.6% done.

Dry networks, TSE and asphalt are far behind

Asphalt is 25,856 m³ against 55,841 m³ planned to date (40.2% of the total). TSE pipes are at 13.5%, LV cables 4.8%, street-light cable 14.9%, telecom ducts 21.3% and MV cable 40.8%. None of the 3 unit substations or 3 RMUs is installed.

Milestones

Baseline and forecast from the weekly report's Milestones sheet; P6 dates and total float from the P6 update with data date 20-Oct-2026.

MILESTONE	BASELINE	WEEKLY REPORT FORECAST	P6 UPDATE FORECAST	P6 FLOAT (DAYS)	STATUS
Site handover	30-Jul-2025	30-Jul-2025	30-Jul-2025 (actual)	–	✓ Done
Complete mobilisation	30-Aug-2025	30-Aug-2025	25-Nov-2025 (actual)	–	✓ Done
Complete earthworks	15-Sep-2026	25-Aug-2026 (−21 d)	–	–	? Forecast date passed
Submittals and long-lead orders complete	24-Sep-2026	24-Oct-2026 (+30 d)	–	–	▼ Late
All equipment and materials delivered	03-Dec-2026	24-Oct-2026 (−40 d)	–	–	? Conflicts with procurement
All wet networks	22-Nov-2026	17-Dec-2026 (+25 d)	17-Dec-2026	63	▼ Late
Electrical works	24-Nov-2026	21-Dec-2026 (+27 d)	30-Dec-2026	53	▼ Late
Potable water pump station	–	–	02-Dec-2026	26	● Scheduled
Sewage lift station	–	–	15-Dec-2026	40	● Scheduled
Road works and asphalt wearing course	–	–	22-Dec-2026	5	▼ At risk
Construction finish	–	–	07-Jan-2027	12	▼ At risk
All works complete, ready for initial handover	14-Jan-2027	14-Feb-2027 (+31 d)	–	–	▼ Late
Complete demobilisation	25-Jan-2027	24-Feb-2027 (+30 d)	–	–	▼ Late
Project handover	29-Jan-2027	01-Mar-2027 (+31 d)	01-Mar-2027	0	▼ Late

The P6 update finishes the project on 01-Mar-2027, 31 days after the contract completion date.

The schedule has no finish constraint at the contract date, so its float is measured against its own late finish and no activity shows negative float. The asphalt wearing course has only 5 days of float and construction finish 12 days. The General Information sheet forecasts completion on 14-Feb-2027 and the look-ahead sheet on 30-Nov-2026, so the three forecasts in the report disagree.

Procurement of key materials

Purchase orders issued and materials on site by discipline. Source: Procurement Summary in the Quality-Stat sheet, weekly report 20-Oct-2026.



Electrical and mechanical deliveries are past their dates


The planned delivery completion was 27-Sep-2026 for electrical and 28-Sep-2026 for mechanical materials, yet only 17 of 30 electrical and 25 of 48 mechanical materials are on site. Civil and roads materials are due by 09-Nov-2026, with 22 of 77 still to arrive.

Pump station, lift station and landscape materials

Purchase orders are issued and manufacturing is under way; supply is about to start (look-ahead sheet). Materials approval: 139 of 155 approved, 7 submittals pending with the consultant.

Manpower

Monthly head count on site (staff plus labour), planned vs actual. Source: Manpower sheet.

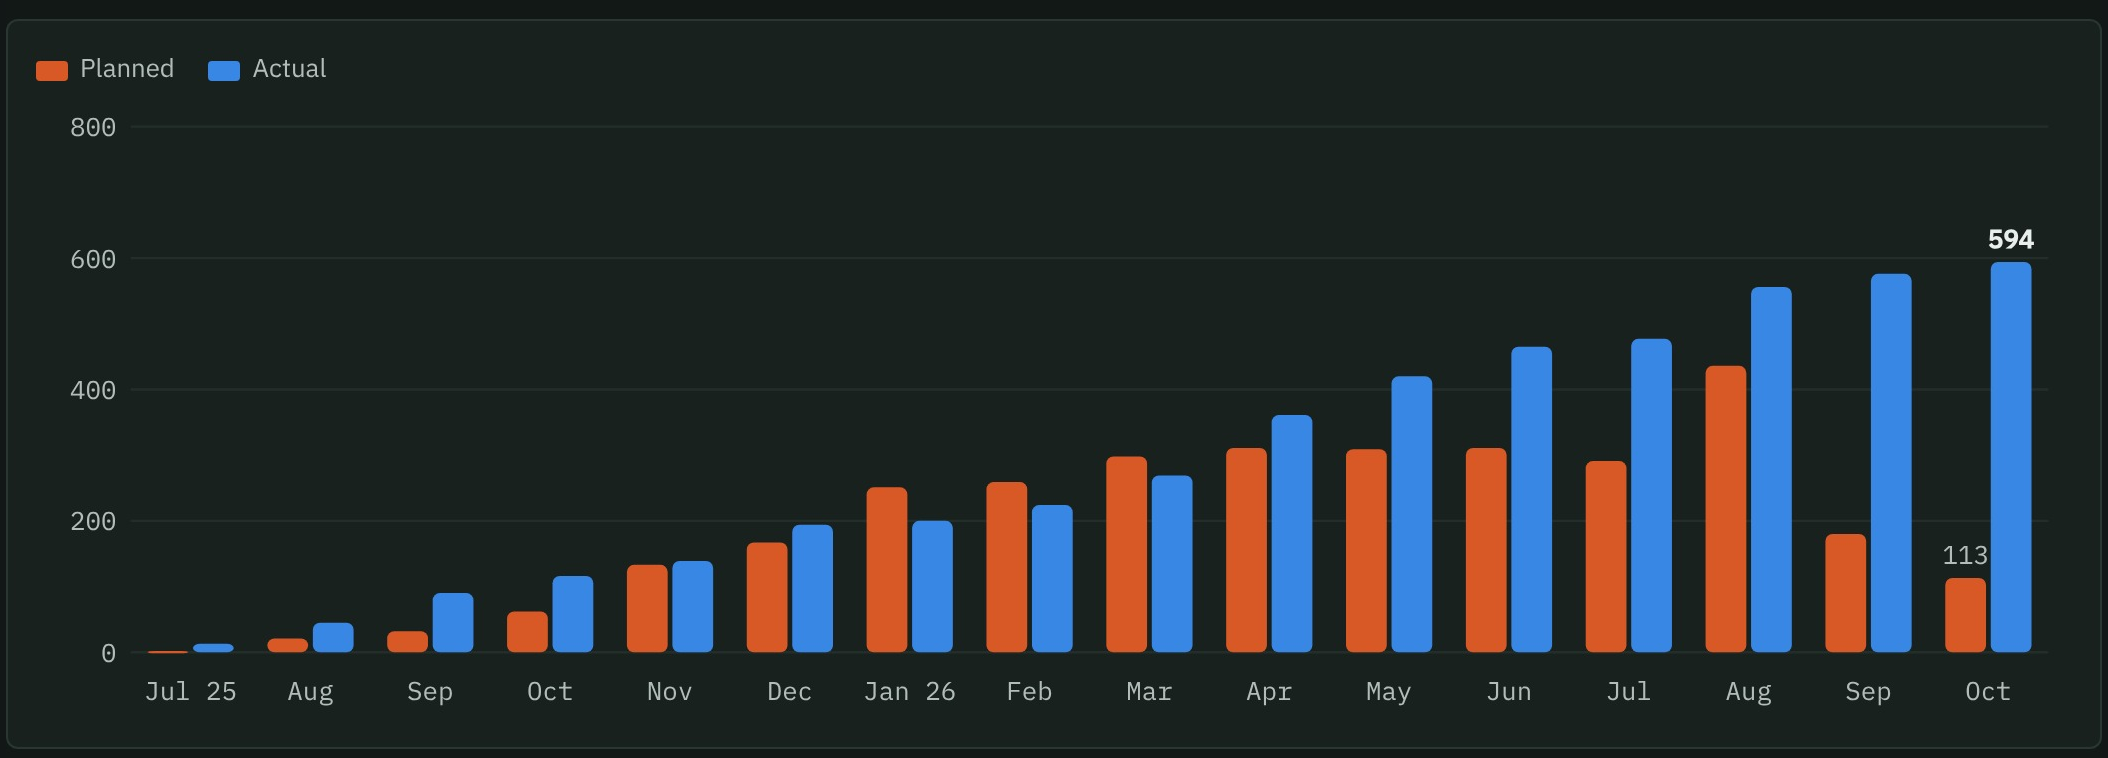

October head count is 594 (57 staff and 537 labour) against 113 planned. The manpower plan peaked at 436 in August 2026 and is falling while the work is behind, so the plan no longer reflects the work left. The contractor forecasts 677 for November. Equipment on site is 326 against 166 planned.

Cost and invoicing

Contract value

Original contract value	198,906,162.61
Revised contract value	198,906,162.61
Change orders	0
Planned value to date (70.7%)	140,538,384.61
Earned value to date (54.5%)	108,337,412.25
FIR value to date (42.4%)	84,260,706.89

All values in SAR. The change order log is empty and potential changes are 0.

Invoices

Invoices submitted	7
Gross value	62,889,673.53
Deductions and penalties	−104,500
Net incl. VAT	72,218,624.56
Approved by consultant (CM)	7
Approved by MODON PM / paid	0 / 0

Invoicing is 31.6% of the contract value against 57.9% physical progress. All seven invoices are approved by the consultant, but none is recorded as approved by the MODON PM or paid. The payment status needs confirming.

Health, safety and quality

Safety Score 0.93

Safe man-hours (cumulative)	874,722
Man-hours this week	34,740
Lost-time injuries	0
Fatalities	0
First-aid cases	0
Near misses	0
Property damage	0
Inductions (cumulative)	148 (895)
Toolbox talks (cumulative)	56 (8,671)

Consultant HSE inspection of 20-Oct-2026. Bracketed figures are as given in the report.

Quality Score 0.93

FIRs issued / closed / pending	4,699 / 4,481 / 218
MIRs issued / closed / pending	116 / 113 / 3
Site instructions issued / closed	52 / 42
NCRs issued / closed	51 / 49
Shop drawings approved	1,774 of 1,774
Materials approved	139 of 155

Consultant quality inspection of 20-Oct-2026. The front page of the report shows 4 NCRs issued and 3 closed; see Data notes.

Open issues and risks

ISSUE	OWNER	DETAIL
Shortage of labour and equipment; subcontractor stopped work	Contractor	Part of the project is being assigned to another contractor and the company is providing its own labour. Labour and equipment must keep increasing to meet MODON's targets. Open since 01-Apr-2026 (202 days).
Culvert on the arterial road delayed	Contractor	Steel fixing is being finished for 16 joints and the base cast for 3; 14 are excavated and 3 more under way. Open since 01-Jun-2026 (141 days).
Networks must be finished before road works	Other	The subcontractor Unasco was removed and its approval withdrawn for not meeting MODON's targets. The contractor must work on the networks directly or submit a new subcontractor for approval. Open since 01-Jun-2026 (141 days).

The risk register lists the same three items, all open and rated high likelihood and high impact after treatment.

Data notes

- Report week: the weekly report states "Current Contract Weeks: 64 of 78" (Milestones sheet). The consultant's HSE and quality inspections use their own numbering (inspection No. 46, counted from 25-Nov-2025).
- This report uses only the latest weekly report (data date 20-Oct-2026). Previous-week quantities are not in it, so the "This week" column of the quantities table shows "—"; the 13-Oct S-curve row is derived from this week's figures.

- Three different completion forecasts: 14-Feb-2027 (General Information sheet, −16 days), 01-Mar-2027 (Milestones sheet and P6 update, −31 days) and 30-Nov-2026 (look-ahead sheet).
- The P6 update has no finish constraint, so no activity shows negative float although it finishes after the contract date. 194 in-progress activities have finish dates before the data date.
- Mobilisation: the weekly report gives 30-Aug-2025 as actual, the P6 milestone "Mobilization - Finish" gives 25-Nov-2025.
- The "Complete earthworks" forecast of 25-Aug-2026 has passed but is still marked as a forecast, with earthworks at 96.2%. The "all materials delivered" forecast of 24-Oct-2026 conflicts with 58 of 155 materials not yet on site.
- The procurement log cannot be used: delivered figures exceed quantities (for example 12,600 delivered of 2 MCCBs, 1,325,000 of 12 DI pipes), many cells show #DIV/0! or #VALUE!, and rows carry project ID DAM2-01-029. The front-page procurement total repeats the mechanical row (48 / 48 / 42) instead of 155 / 155 / 140, and shows 1 remaining PO against 15 implied.
- NCRs: the front page shows 4 issued and 3 closed; the Quality-Stat sheet shows 51 issued and 49 closed.
- Labour: the front page shows 360 planned and 483 actual; the Manpower sheet shows 78 planned and 537 actual for October, and its trade table plans 391.
- Scope quantities in the Conclusion sheet differ from the Major Quantities sheet (sewer total 6,146 vs 7,567 LM, TSE total 17,678 vs 57,419 LM, telecom finished 1,000 vs 2,358 LM). Sewer pipes show 2.01 LM planned to date, and manholes and catch basins have fractional totals (for example 135.99).
- Contract value is 198,906,162.61 on the front page and 198,906,162.312 "incl. VAT" in the Conclusion sheet. The invoice log has stray values (21,100,000, 20,900,000, 200,000) beside the contract values, and EAC shows #REF!.
- Key submittal dates (quality, safety and baseline plans) are in Feb–Mar 2024, before the contract award of 30-Jun-2025. The look-ahead sheet contains P6 data from the Hail Industrial City Phase II project, and the risk register uses project ID DAM2-01-029 and names the 3rd and 6th Industrial Cities.
- The action text of issue 1 still quotes 304 workers and 184 items of equipment, against 594 and 326 now on site.
- Landscape shows 31.6% physical progress, mostly procurement credit, against 0.7% of its value earned.

Compiled 28-Oct-2026 from the weekly report with data date 20-Oct-2026 and its P6 update.
