MODON - Weekly Progress Report - Construction Projects

Data Date 26-Oct-26

Contract General Information

Project Name	Playground Initiative for Western Region (Asir - Jazan - Jeddah)			Contract Award	04-Feb-26	Contract Award (Hijri)	16-08-1447
Project ID	MLTX-02-004	Stage	Construction	Contract Sign	04-Mar-26	Contract Sign (Hijri)	15-09-1447
Contractor	Profast Company Ltd.	Status	Active	Site Handover	26-Mar-26	Site Handover (Hijri)	07-10-1447
Consultant	Saudi Arabia Consulting Engineering Company "EGIS"	Modon PM	Engr.Yazeed Al Ragabh	Original Completion	25-Jan-27	Original Completion (Hijri)	17-08-1448

Revised Completion	25-Jan-27		
Committed Completion	25-Jan-27		
Forecast Completion	19-May-27		
Variance	(114)		

Cost Summary (SR)

Original Contract Value	33,997,787	O&M Value	0
Revised Contract Value	33,793,604	Revised O&M Value	0
Estimate At Completion Value	33,997,787	Submitted Invoices (Gross Value)	4,943,711
Potential Changes	(204,183)	Total Deduction	11,000

Performance Summary

Plan Value	43.35%	Phys. Plan Value	76.10%	Quality Score	85.7%
Earn Value	37.63%	Phys. Earn Value	60.74%		
Variance	(5.72%)	Variance	(15.36%)	Safety Score	83.8%
SPI	0.87	SPI	0.80		

Project Scope

The Scope of Works for the Playground Initiative for Western Region (ASIR - JAZAN – JEDDAH) according to the following contents.
-Playground Area (Padel – Basketball – football)
-Service & Toilet Building
-Land Scape Works
-Bike & Walking Paths
-Parking

Progress Overview


Earned Value Progress (SAR)


WBS	BOQ Value (SAR)	% Wt.	Weekly (SAR) Planned	Weekly (SAR) Earned	To Date (SAR) Original Plan	To Date (SAR) Revised Planned	To Date (SAR) Earned	Original Plan %	Revised Planned %	Earned %	Variance	SPI
-	-	0.0%	-	-	-	-	-	0.0%	0.0%	0.0%	0.0%	
Mobilization	-	0.0%	-	-	-	-	-	0.0%	0.0%	0.0%	0.0%	
Engineering	-	0.0%	-	-	-	-	-	0.0%	0.0%	0.0%	0.0%	
Procurement	-	0.0%	-	-	-	-	-	0.0%	0.0%	0.0%	0.0%	
Construction	33,793,604	100.0%	1,424,245	755,897	3,561,002	14,647,968	12,715,612	10.5%	43.3%	37.6%	-5.7%	0.87
Jazan Region	10,680,072	31.6%	238,913	416,706	794,326	4,190,272	3,085,789	7.4%	39.2%	28.9%	-10.3%	0.74
Asir Region	10,578,073	31.3%	579,937	145,358	1,310,370	3,643,214	4,194,757	12.4%	34.4%	39.7%	5.2%	1.15
Jeddah Region	12,535,460	37.1%	605,394	193,834	1,456,306	6,814,482	5,435,065	11.6%	54.4%	43.4%	-11.0%	0.80
Testing & Commissioning	-	0.0%	-	-	-	-	-	0.0%	0.0%	0.0%	0.0%	
Close-Out	-	0.0%	-	-	-	-	-	0.0%	0.0%	0.0%	0.0%	
	-	0.0%	-	-	-	-	-	0.0%	0.0%	0.0%	0.0%	
	-	0.0%	-	-	-	-	-	0.0%	0.0%	0.0%	0.0%	
	-	0.0%	-	-	-	-	-	0.0%	0.0%	0.0%	0.0%	
	-	0.0%	-	-	-	-	-	0.0%	0.0%	0.0%	0.0%	
	-	0.0%	-	-	-	-	-	0.0%	0.0%	0.0%	0.0%	
Total	**33,793,604**	**100.0%**	**2,848,490**	**1,511,795**	**3,561,002**	**14,647,968**	**12,715,612**	**10.54%**	**43.35%**	**37.63%**	**-5.72%**	**0.87**


Physical Progress (Effort)

	Budgeted (Manhours)	% Wt.	Weekly Physical Progress Planned	Weekly Physical Progress Earned	To Date Physical Progress Plan %	To Date Physical Progress Earned %	Planned	Earned	Plan %	Earned %	Variance	SPI
Mobilization	12,659	3.1%	-	-	0.0%	0.0%	12,659	12,659	100.0%	100.0%	0.0%	1.00
Engineering	21,299	5.2%	-	-	0.0%	0.0%	21,300	21,010	100.0%	98.6%	-1.4%	0.99
Procurement	51,273	12.6%	85	-	0.2%	0.0%	50,817	31,870	99.1%	62.2%	-37.0%	0.63
Construction	299,660	73.8%	16,994	8,908	5.7%	3.0%	139,599	115,667	46.6%	38.6%	-8.0%	0.83
Jazan Region	102,280	25.2%	5,016	6,293	4.9%	6.2%	50,548	31,118	49.4%	30.4%	-19.0%	0.62
Asir Region	96,810	23.8%	5,560	794	5.7%	0.8%	46,031	40,367	47.5%	41.7%	-5.9%	0.88
Jeddah Region	100,570	24.8%	6,418	1,821	6.4%	1.8%	43,020	44,182	42.8%	43.9%	1.2%	1.03
Testing & Commissioning	12,818	3.2%	-	-	0.0%	0.0%	-	-	0.0%	0.0%	0.0%	
Close-Out	8,546	2.1%	-	-	0.0%	0.0%	-	-	0.0%	0.0%	0.0%	
	-	0.0%	-	65,539	0.0%	0.0%	84,775	65,539	0.0%	0.0%	0.0%	
	-	0.0%	-	-	0.0%	0.0%	-	-	0.0%	0.0%	0.0%	
	-	0.0%	-	-	0.0%	0.0%	-	-	0.0%	0.0%	0.0%	
	-	0.0%	-	-	0.0%	0.0%	-	-	0.0%	0.0%	0.0%	
	-	0.0%	-	-	0.0%	0.0%	-	-	0.0%	0.0%	0.0%	
	-	0.0%	-	-	0.0%	0.0%	-	-	0.0%	0.0%	0.0%	
Total	**406,255**	**100.0%**	**17,079**	**74,446**	**4.20%**	**18.33%**	**309,150**	**246,745**	**76.10%**	**60.74%**	**-15.36%**	**0.80**

Earned Value Progress (%)



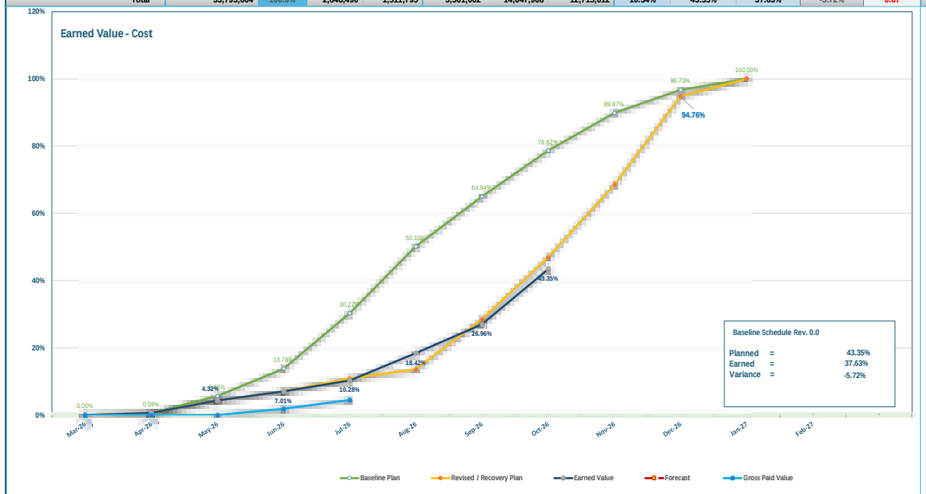

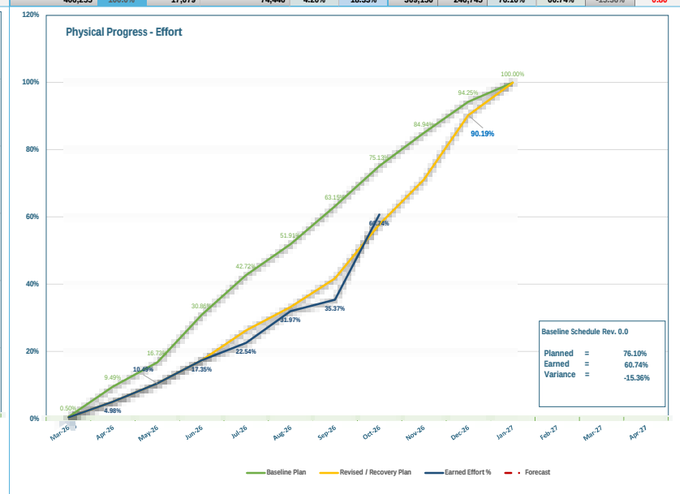


Construction Milestones

Item No.	Milestones	Original (Baseline)	Latest Plan	Forecast	Status	Days Change
1	Project Finish	25-Jan-27	19-May-27	**19-May-27**	F	(114)
2	Project Start	26-Mar-26	26-Mar-26	**26-Mar-26**	A	0
3	Baseline Programme Approval	29-Apr-26	29-Apr-26	**29-Apr-26**	A	0
4	Completion of Mobilization	02-Jun-26	02-Jun-26	**02-Jun-26**	A	0
5	Completion of Levelling Works	22-Jul-26	27-Oct-26	**27-Oct-26**	F	(97)
6	Completion of Engineering	19-Jan-27	12-Nov-26	**12-Nov-26**	F	68
7	Completion of Toilet Building	09-Aug-26	11-Jan-27	**11-Jan-27**	F	(156)
8	Completion of Natural Landscape Works	16-Jan-27	18-Mar-27	**18-Mar-27**	F	(61)
9	Completion of Playground Area	30-Nov-26	06-May-27	**06-May-27**	F	(157)
10	Completion of Asir Works	13-Dec-26	05-Apr-27	**05-Apr-27**	F	(113)


This Week

Project Status Score



Actual Invoices

Average Invoice Value: 988,742



Performance overview

Submittals Status

Shop Drawings

Item Per WBS	Total	Total Submitted Drawings A	B	C	D	Processed	Remaining	Pending	Total Submittals
Civil/Structure	37	6	27	1	3	37	0	3	40
Architecture	20	4	14	1	0	19	0	1	20
Mechanical	25	0	19	5	1	25	0	0	25
Electrical	37	0	34	0	3	37	0	0	37
Landscape	23	7	14	2	0	23	0	0	23
TOTAL	142	17	108	9	7	141	0	4	145

Material Approval

Item Per WBS	Total	Total Submitted Material A	B	C	D	Processed	Remaining to approve	Pending	Total Submittals
Civil/Structure	52	2	40	7	2	42	0	1	51
Architecture	26	2	24	0	0	26	0	0	26
Mechanical	33	0	31	2	0	31	0	0	33
Electrical	36	0	31	4	1	31	0	1	37
TOTAL	147	4	126	13	3	130	0	2	147

Procurement Summary

Item Per WBS	Total Materials Planned	Total Number of P.O.	Actual P.O. To Date	Remaining P.O	Actual Material on Site	Remaining Materials	Material Delivery Completion (Date)
Civil/Structure	22	27	5	22	5	22	00-Jan-00
Architecture	30	18	14	4	7	11	00-Jan-00
Mechanical	30	18	10	8	7	11	00-Jan-00
Electrical	35	13	6	7	3	10	00-Jan-00
TOTAL	117	76	35	41	22	54	00-Jan-00

Primavera P6 Schedule Status

Project Activities Overview

Schedule Statistics Total Act.	Not Started	In Progress	Completed	%	Active	Ahead	On	Behind	Flag	0
2,134	371	26	1,737	81.40%	26	34	135	248		(70)

Critical Path Activities Last Week	This Week	Diff	Free Float Management (Total) Greater Than 14 Days Last Week	This Week	Less Than 14 Days Last Week	This Week	Failed Start Activities Last Week	This Week	Flag	0
331	320	11	66	69	340	328	240	236		4

Quality

Quality Reports

Quality Reports	Issued	Closed	Pending	Avg. Closing (Days)	Pending 0-10 Days	11-20 Days	21-30 Days	31-60 Days	> 60 Days
Non Conformance (NCR)	23	33	1	0	2	0	0	0	0
Site Instruction (SIR)	27	25	2	0	0	3	0	0	0
Material Inspection (MIR)	106	103	3	0	11	0	0	0	0
Field Inspection (FIR)	704	683	19	0	46	0	0	0	0

Key Submittals Approval Status

1 Quality Plan Approval	30-Apr-26	6 Baseline Approval	28-Apr-26
2 Quality Plan Last Up	-	7 No of Approved Version of Schedule	-
3 Safety Plan Approval	11-Jun-26	8 Last Approved Schedule	-
4 Safety Plan Last Up	-	9 BOQ Approval Date	18-Sep-25
5 Construction Plan Approval	13-May-26	10 No of Approved Version of BOQ	0

Invoices Summary

Total Submitted Invoices	5	Submitted Invoices (SAR)	4,943,711
PM Approved Invoices	0	PM Approved Invoices (SAR)	0
No of Paid Invoices	0	Paid Invoices (SAR)	0
No of Pending Invoices	5	Last Submitted Period	08-Oct-26
Advance Payment %	0%	Advance Payment (SAR)	0
Retention %	0%	Retention (SAR)	0
Deduction / Penalties %	0%	Deduction / Penalties (SAR)	11,000



Resources at Site

Head Count - Manual Planned	Actual	Next Month Forecast	Saudi Staff	Head Count - Non Manual Planned	Actual	Next Month Forecast	Saudi Staff	Total Head Count Total Plan	Total Actual	Variance
175	77	140	0	19	30	25	0	194	107	-87

Manpower Breakdown by Trade

Key Trade	Planned	Actual
Labor	65	22
Skilled Labor	25	10
Driver / Operator	27	12
Carpenter	0	6
Steel Fixer	26	6
Mason	0	0
Plumber	0	3
Total	175	77



Major Equipment

Type	Planned	Actual	Idle
Excavator	3	3	0
Bulldozer	2	0	0
Grader	3	0	0
Road Roller	1	0	0
Crane	0	0	0
Bobcat	0	5	0
Other	0	0	0
Total	9	8	0

Safety


Safety Statistics

Category	Item	This Month	Year to Date	Cumulative
General	Total Hours Worked	6,480	6,480	132,050	132,050
	Safe Hours Worked	6,480	6,480	132,050	132,050
Reactive	LTI	0	0	0	0
	MTC (Healed w/o Disability)	0	0	0	0
	MTC (Healed w/ Disability)	0	0	0	0
	Near Miss	0	0	0	0
	First Aid Cases	0	0	0	0
	Fatality	0	0	0	0
	Fire Incident Cases	0	0	0	0
	Vehicle Incident	0	0	0	0
	Property Damages	0	0	0	0
Proactive	Induction Training	0	18	160	160
	No.of Internal Training	1	04 Session	17 Session	17 Session
	No.of Internal Audit	0	0	0	0
	No. of Toolbox Talks	4	4 Sessions	156 sessions	156 sessions
	Safety Awards/Incentives	0	0	0	0

Proactive Vs Reactive Actions Taken



Total Hours Worked Vs Safe Hours Worked



Latest Contract Change Order Log

CCO No.	Date Added	Description of Change	Status	Cost	Sch Impact (Months)	Date Approved	Duration
-	-	-	-	-	-	-	-

Major Quantity Trackers

BOQ NO.	Item Description	Total Qty	Measu Unit	Plan to Date	Act to Date	Remaining	Variance
2.3.1	Supply and plant trees	895	Nos.	0.00	0.00	30380.00	0.00
2.3.10	Supply and cast Concrete	145	m^3	0.00	0.00	248.00	0.00
9.1.1	CEILING FINISHES	207	m^2	0.00	0.00	219.00	0.00
9.3	WATER SUPPLY SYSTEMfor cold and hot water supply piping	138	Lm	0.00	0.00	207.00	0.00
15.2.1	SEWER AND DRAINAGE PIPE	177	Lm	0.00	14.00	124.00	14.00

Testing And Commissioning

Item	Planned Start Date	Planned Finish Date	Forecast Start Date	Forecast Finish Date	Actual Start Date	Actual Finish Date	% Completed	Open Comments	Closed Comments
TESTING & COMMISSIONING JEDDAH	08-Dec-26	01-Apr-27	08-Dec-26	01-Apr-27					
TESTING & COMMISSIONING ASIR	30-Jan-27	18-Apr-27	30-Jan-27	18-Apr-27					
TESTING & COMMISSIONING JAZAN	28-Jan-27	15-Apr-27	28-Jan-27	15-Apr-27					

Top Issues and Risks

Top 5 Issues

Issue No	Date Identified	Issue Description	Responsible	Action Taken	Mitigation	Current Status	Expected/Actual Closure	Duration Elapsed
1		Connection of the project to the drainage channel on the eastern side.(Jeddah)	Contractor	Coordination between the Municipality (City Management) and the infrastructure contractor.		Completed	2026-05-21	
2		drainage pipe was encountered during site excavation.(Jeddah)	Owner	The required calculations and slope analysis have been completed.		Completed	2026-05-21	
3	05-May-26	Based on the visit by Modon management, it was noted that the project level can be raised to	Owner	The required filling quantity was estimated at 59,000 m^3		Completed	2026-05-21	
4		Increase the sewage tank capacity for the Asir project to serve the administration building and	Contractor	Waiting for clarification of the project savings/cost reductions.		Completed	2026-05-10	
5	21-May-26	Difficulty accessing the parking area due to a level difference-Jazan	Consultant	Relocating the parking area to the far left side.		Completed	2026-05-16	
6	13-05-2026	Road shoulder overlap at the Jeddah site	Consultant	A proposal has been submitted to the consultant.		Completed	2026-10-01	
7	06-Feb-26	Trees located within Asir site.	Owner	Waiting for tree removal by the landscaping contractor.		Completed	2026-05-16	
	10-Oct-26	Medium voltage cables on excavatio	Owner	Medium voltage cables are conflicting with the excavation route. Assessment and coordination with relevant stakeholders are ongoing to determine the required mitigation		Open		

Data sensitivity - Public
