
Development of the Technology City in Dammam -Upda
10-11-2026
WPR UPS LEVEL 5


Activity ID	Activity Name	Original Duration	BL Project Start	BL Project Finish	Start	Finish	BL Project Total Cost	Earned Value Cost	Schedule % Complete	Performance % Complete
Development of the Technology City in Dammam -Update 10-11-2026		438	23-Dec-25	24-Feb-27	23-Dec-25 A	21-Jun-27	67,768,369.77	26,571,844.57	44.6%	39.21%
Key Milestones		438	23-Dec-25	24-Feb-27	23-Dec-25 A	21-Jun-27	0.00	0.00	0%	0%
Contractual Milestones		438	23-Dec-25	24-Feb-27	23-Dec-25 A	21-Jun-27	0.00	0.00	0%	0%
MS-CF-IR	Completion of Construction Works for Irrigation Network	0		03-Jan-27		14-Apr-27	0.00	0.00	0%	0%
MS-CF-MV	Completion of Construction Works for Medium Voltage Network	0		11-Jan-27		05-May-27	0.00	0.00	0%	0%
MS-CF-PW	Completion of Construction Works for Potable Water Network	0		28-Jan-27		29-Apr-27	0.00	0.00	0%	0%
MS-CF-RD	Completion of Construction Works for Road Works	0		16-Feb-27		05-Jun-27	0.00	0.00	0%	0%
MS-CF-SW	Completion of Construction Works for Sewage Network	0		13-Jan-27		22-Feb-27	0.00	0.00	0%	0%
MS-CF-SD	Completion of Construction Works for Storm Drainage Network	0		03-Jan-27		06-Apr-27	0.00	0.00	0%	0%
MS-CF-SL	Completion of Construction Works for Street Lighting Network	0		27-Jan-27		12-May-27	0.00	0.00	0%	0%
MS-CF-TE	Completion of Construction Works for Telecom Network	0		20-Jan-27		22-May-27	0.00	0.00	0%	0%
MS-CF-TSE	Completion of Construction Works for Treated Sewage Effluent Network	0		17-Jan-27		28-Apr-27	0.00	0.00	0%	0%
MS-CF-EBL	Completion of Execution Plan and Baseline Schedule	0		23-Jun-26		18-Jan-26 A	0.00	0.00	100%	100%
MS-CF-MOB	Completion of Mobilization and Site Preperation Works	0		23-Jun-26		18-Jan-26 A	0.00	0.00	100%	100%
MS-CF-ENG	Completion of Submitting and Approval of Shopdrwing and Material	0		14-Jul-26		21-Aug-26 A	0.00	0.00	100%	100%
MS-CS-PS	Project Commencement Date (Site Handover)	0	23-Dec-25		23-Dec-25 A		0.00	0.00	100%	100%
MS-CF-PF	Project Completion Date	0		24-Feb-27		21-Jun-27	0.00	0.00	0%	0%
Preliminaries and Mobilization Works		30	23-Dec-25	27-Jan-26	23-Dec-25 A	26-Jan-26 A	0.00	0.00	0%	0%
Mobilization Works		30	23-Dec-25	27-Jan-26	23-Dec-25 A	26-Jan-26 A	0.00	0.00	0%	0%
MOB-10	Clear and Grub for Offices and Access Roads	23	31-Dec-25	26-Jan-26	31-Dec-25 A	26-Jan-26 A	0.00	0.00	100%	100%
MOB-40	Construction Project Store	23	31-Dec-25	26-Jan-26	31-Dec-25 A	26-Jan-26 A	0.00	0.00	100%	100%
MOB-80	Construction Site Access Roads	29	23-Dec-25	25-Jan-26	23-Dec-25 A	26-Jan-26 A	0.00	0.00	100%	100%
MOB-70	Installation Project Sign Board	13	12-Jan-26	26-Jan-26	12-Jan-26 A	26-Jan-26 A	0.00	0.00	100%	100%
MOB-60	Mobilization of Major Equipments	23	31-Dec-25	27-Jan-26	31-Dec-25 A	26-Jan-26 A	0.00	0.00	100%	100%
MOB-50	Mobilization of Major Manpower	23	31-Dec-25	27-Jan-26	31-Dec-25 A	26-Jan-26 A	0.00	0.00	100%	100%
MOB-20	Project Site Layout Plan Approval	6	23-Dec-25	30-Dec-25	23-Dec-25 A	29-Dec-25 A	0.00	0.00	100%	100%
MOB-90	Site Surveying Work	30	23-Dec-25	26-Jan-26	23-Dec-25 A	26-Jan-26 A	0.00	0.00	100%	100%
MOB-30	Supply & Install of Project Supervision Offices	29	23-Dec-25	25-Jan-26	23-Dec-25 A	26-Jan-26 A	0.00	0.00	100%	100%
Project Main Documents From The Contractor		23	23-Dec-25	19-Jan-26	23-Dec-25 A	18-Jan-26 A	0.00	0.00	0%	0%
PRE-CON-MDC-2	Submission Project Baseline Schedule	23	23-Dec-25	19-Jan-26	23-Dec-25 A	18-Jan-26 A	0.00	0.00	100%	100%
PRE-CON-MDC-7	Submission Project Environmental Plan	23	23-Dec-25	19-Jan-26	23-Dec-25 A	18-Jan-26 A	0.00	0.00	100%	100%
PRE-CON-MDC-1	Submission Project Execution Plan	23	23-Dec-25	19-Jan-26	23-Dec-25 A	18-Jan-26 A	0.00	0.00	100%	100%
PRE-CON-MDC-6	Submission Project Geotechnical Soil Report	23	23-Dec-25	19-Jan-26	23-Dec-25 A	18-Jan-26 A	0.00	0.00	100%	100%
PRE-CON-MDC-3	Submission Project Health & Safety Plan	23	23-Dec-25	19-Jan-26	23-Dec-25 A	18-Jan-26 A	0.00	0.00	100%	100%
PRE-CON-MDC-8	Submission Project Organization Chart and Communications Plan	23	23-Dec-25	19-Jan-26	23-Dec-25 A	18-Jan-26 A	0.00	0.00	100%	100%
PRE-CON-MDC-4	Submission Project Quality Control Plan	23	23-Dec-25	19-Jan-26	23-Dec-25 A	18-Jan-26 A	0.00	0.00	100%	100%
PRE-CON-MDC-5	Submission Project Surveying Report	23	23-Dec-25	19-Jan-26	23-Dec-25 A	18-Jan-26 A	0.00	0.00	100%	100%

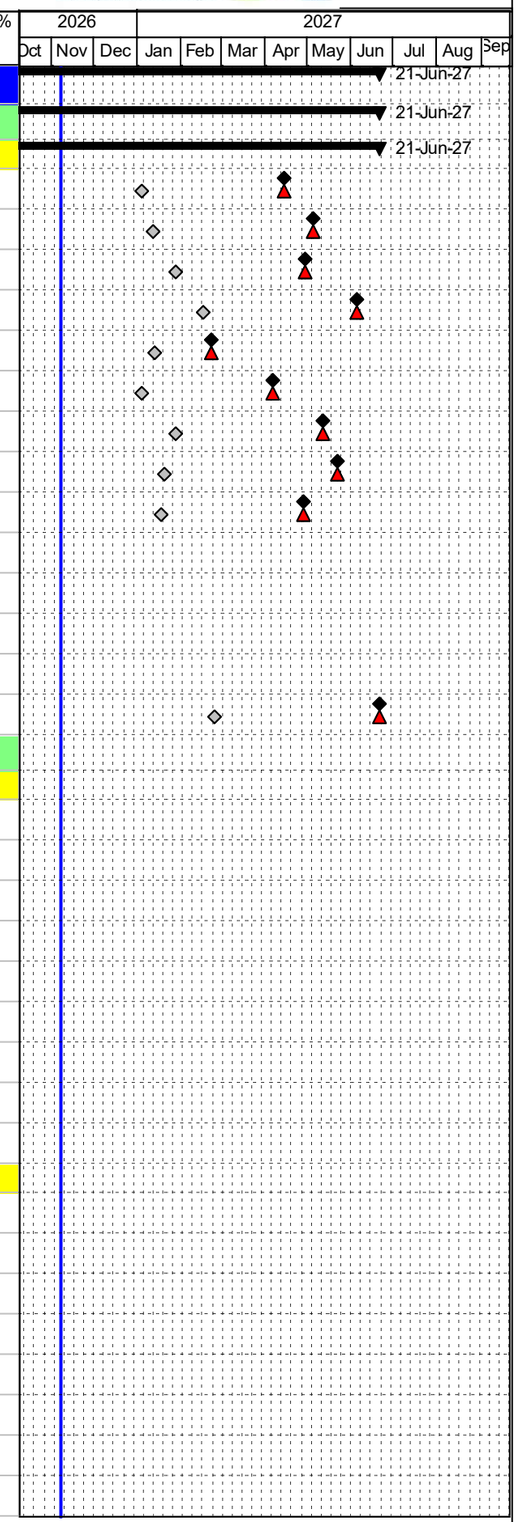

Primary Baseline
Remaining Work
Critical Remaining Work
Actual Work
Baseline Milestone
Milestone
Summary

Date	Revision	Checked	Approved
10-Nov-26	Third Industrial City		


Activity ID	Activity Name	Original Duration	BL Project Start	BL Project Finish	Start	Finish	BL Project Total Cost	Earned Value Cost	Schedule % Complete	Performance % Complete
Engineering Works		239	06-Jan-26	14-Jul-26	06-Jan-26 A	20-Aug-26 A	0.00	0.00	0%	0%
Shop Drawings		138	17-Jan-26	14-Jul-26	17-Jan-26 A	13-Jul-26 A	0.00	0.00	0%	0%
Infrastructure Networks		138	17-Jan-26	14-Jul-26	17-Jan-26 A	13-Jul-26 A	0.00	0.00	0%	0%
Road Works		138	17-Jan-26	13-Jul-26	17-Jan-26 A	13-Jul-26 A	0.00	0.00	0%	0%
Sewage Network		128	17-Jan-26	30-Jun-26	17-Jan-26 A	30-Jun-26 A	0.00	0.00	0%	0%
Storm Drainage Network		132	17-Jan-26	06-Jul-26	17-Jan-26 A	06-Jul-26 A	0.00	0.00	0%	0%
Potable Water Network		132	18-Jan-26	06-Jul-26	18-Jan-26 A	06-Jul-26 A	0.00	0.00	0%	0%
Irrigation Network		13	23-Jun-26	07-Jul-26	23-Jun-26 A	07-Jul-26 A	0.00	0.00	0%	0%
Treated Sewage Effluent Network		13	23-Jun-26	07-Jul-26	23-Jun-26 A	07-Jul-26 A	0.00	0.00	0%	0%
Medium Voltage Network		134	17-Jan-26	07-Jul-26	17-Jan-26 A	07-Jul-26 A	0.00	0.00	0%	0%
Low Voltage Network		13	23-Jun-26	07-Jul-26	23-Jun-26 A	07-Jul-26 A	0.00	0.00	0%	0%
Street Lighting Network		130	17-Jan-26	02-Jul-26	17-Jan-26 A	02-Jul-26 A	0.00	0.00	0%	0%
Telecom Network		8	30-Jun-26	14-Jul-26	29-Jun-26 A	07-Jul-26 A	0.00	0.00	0%	0%
Superstructure Works		134	17-Jan-26	07-Jul-26	17-Jan-26 A	07-Jul-26 A	0.00	0.00	0%	0%
Pump Stations		130	17-Jan-26	02-Jul-26	17-Jan-26 A	02-Jul-26 A	0.00	0.00	0%	0%
Lift Station		130	17-Jan-26	02-Jul-26	17-Jan-26 A	02-Jul-26 A	0.00	0.00	0%	0%
Storm Drainage Ponds		7	28-Jun-26	06-Jul-26	28-Jun-26 A	06-Jul-26 A	0.00	0.00	0%	0%
Storage Tank (TSE)		7	30-Jun-26	07-Jul-26	30-Jun-26 A	07-Jul-26 A	0.00	0.00	0%	0%
Gaurd Room		6	23-Jun-26	29-Jun-26	23-Jun-26 A	29-Jun-26 A	0.00	0.00	0%	0%
Fence		114	29-Jan-26	28-Jun-26	29-Jan-26 A	28-Jun-26 A	0.00	0.00	0%	0%
Material Submittals and Approvals		239	06-Jan-26	12-Jul-26	06-Jan-26 A	20-Aug-26 A	0.00	0.00	0%	0%
Short Lead Time Items		238	06-Jan-26	12-Jul-26	06-Jan-26 A	12-Jul-26 A	0.00	0.00	0%	0%
Infrastructure Networks		146	06-Jan-26	12-Jul-26	06-Jan-26 A	12-Jul-26 A	0.00	0.00	0%	0%
Superstructure Works		230	15-Jan-26	30-Jun-26	15-Jan-26 A	08-Mar-26 A	0.00	0.00	0%	0%
Long Lead Time Items		231	15-Jan-26	02-Jul-26	15-Jan-26 A	20-Aug-26 A	0.00	0.00	0%	0%
Infrastructure Networks		3	15-Jan-26	19-Jan-26	15-Jan-26 A	22-Jan-26 A	0.00	0.00	0%	0%
Superstructure Works		8	24-Jun-26	02-Jul-26	17-Jun-26 A	20-Aug-26 A	0.00	0.00	0%	0%
Procurement Cycle		377	28-Jan-26	28-Jan-27	28-Jan-26 A	11-May-27	0.00	0.00	0%	0%
Short Lead Time Items		358	28-Jan-26	28-Jan-27	28-Jan-26 A	18-Apr-27	0.00	0.00	0%	0%
Infrastructure Networks		358	28-Jan-26	28-Jan-27	28-Jan-26 A	18-Apr-27	0.00	0.00	0%	0%
Road Works		140	23-Jun-26	05-Dec-26	23-Jun-26 A	08-Nov-26	0.00	0.00	0%	0%
Softscape and Planting Works		104	11-Jul-26	10-Nov-26	08-Nov-26	18-Mar-27	0.00	0.00	0%	0%
Sewage Network		304	23-Jun-26	28-Dec-26	03-Mar-26 A	13-Jan-27	0.00	0.00	0%	0%
Storm Drainage Network		227	23-Jun-26	10-Dec-26	03-Mar-26 A	18-Apr-27	0.00	0.00	0%	0%
Potable Water Network		313	01-Apr-26	13-Dec-26	01-Apr-26 A	18-Apr-27	0.00	0.00	0%	0%
Irrigation Network		316	28-Jan-26	27-Oct-26	28-Jan-26 A	22-Feb-27	0.00	0.00	0%	0%
Treated Sewage Effluent (Tse)		271	01-Apr-26	10-Oct-26	03-Mar-26 A	22-Feb-27	0.00	0.00	0%	0%
Medium Voltage Network		127	23-Jun-26	05-Dec-26	08-Nov-26	14-Apr-27	0.00	0.00	0%	0%
Low Voltage and Street Lighting Network		130	23-Jun-26	28-Jan-27	13-May-26 A	24-Dec-26	0.00	0.00	0%	0%
Telecom Network		92	07-Jul-26	24-Oct-26	08-Nov-26	28-Feb-27	0.00	0.00	0%	0%
Superstructure Works		304	29-Jan-26	11-Oct-26	29-Jan-26 A	06-Feb-27	0.00	0.00	0%	0%
Issuance of Purchase Orders		229	29-Jan-26	13-Jul-26	29-Jan-26 A	27-Aug-26 A	0.00	0.00	0%	0%
Manufacturing of Material		216	23-Jun-26	11-Oct-26	05-Jul-26 A	05-Feb-27	0.00	0.00	0%	0%
1st Material Delivery & Site Inspection		96	02-Aug-26	08-Oct-26	03-Aug-26 A	08-Nov-26	0.00	0.00	0%	0%
Material Delivery & Site Inspection		167	25-Jul-26	11-Oct-26	02-Aug-26 A	06-Feb-27	0.00	0.00	0%	0%
Long Lead Time Items		163	23-Jun-26	23-Dec-26	22-Jul-26 A	11-May-27	0.00	0.00	0%	0%
Infrastructure Networks		108	23-Jun-26	31-Oct-26	08-Nov-26	23-Mar-27	0.00	0.00	0%	0%
CCTV System Wroks of Telecom Network		108	23-Jun-26	31-Oct-26	08-Nov-26	23-Mar-27	0.00	0.00	0%	0%
Superstructure Works		163	04-Jul-26	23-Dec-26	22-Jul-26 A	11-May-27	0.00	0.00	0%	0%
Pump Stations		97	04-Jul-26	20-Dec-26	22-Jul-26 A	14-Feb-27	0.00	0.00	0%	0%
Lift Stations		134	04-Jul-26	23-Dec-26	22-Jul-26 A	06-Apr-27	0.00	0.00	0%	0%
Storage Tank (TSE)		149	04-Jul-26	23-Dec-26	08-Nov-26	11-May-27	0.00	0.00	0%	0%
Construction Works		366	07-Mar-26	23-Feb-27	07-Mar-26 A	05-Jun-27	67,768,369.77	26,571,844.57	44.6%	39.21%
Infrastructure Networks		366	07-Mar-26	16-Feb-27	07-Mar-26 A	05-Jun-27	27,934,729.42	7,809,941.11	42.77%	27.96%
Earthworks		117	07-Mar-26	02-Aug-26	07-Mar-26 A	08-Nov-26	5,376,162.05	5,310,198.54	100%	98.77%

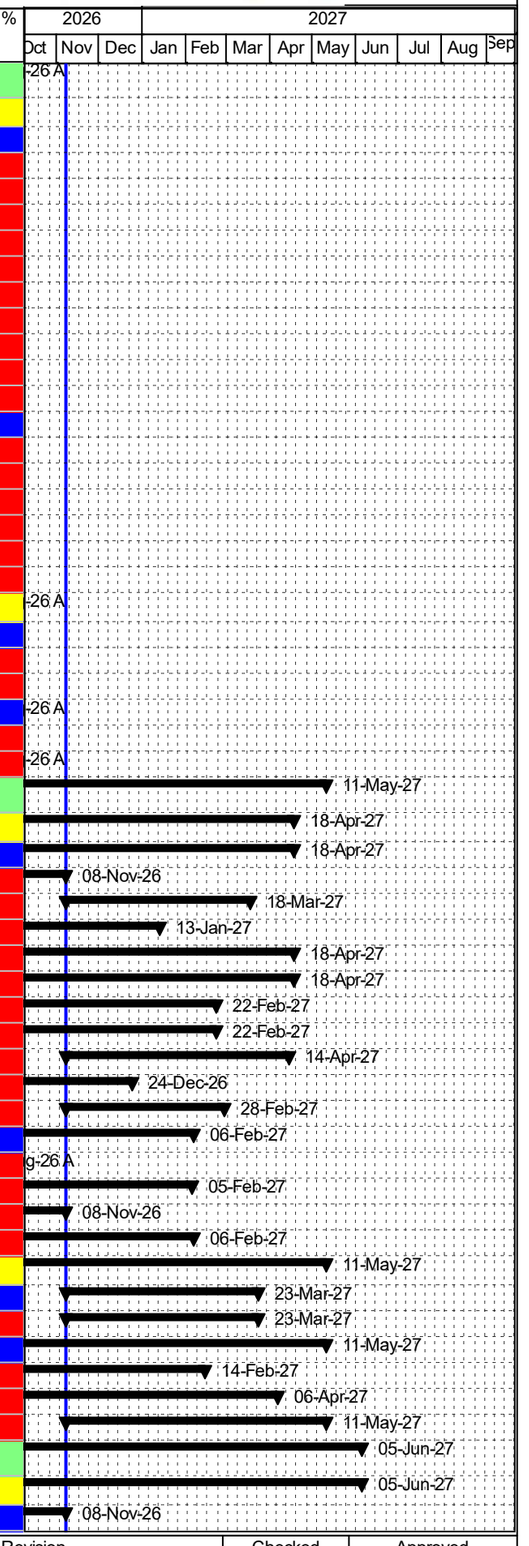

Primary Baseline | Actual Work | Summary
Remaining Work | Baseline Milestone
Critical Remaining Work | Milestone

Date	Revision	Checked	Approved
10-Nov-26	Third Industrial City		

Activity ID	Activity Name	Original Duration	BL Project Start	BL Project Finish	Start	Finish	BL Project Total Cost	Earned Value Cost	Schedule % Complete	Performance % Complete
Earthworks		117	07-Mar-26	02-Aug-26	07-Mar-26 A	08-Nov-26	5,376,162.05	5,310,198.54	100%	98.77%
Storm Drainage Network		168	15-Jul-26	01-Nov-26	02-Aug-26 A	27-Jan-27	4,958,378.40	1,986,162.33	100%	40.06%
FROM MH-25:MH-12		134	15-Jul-26	30-Sep-26	02-Aug-26 A	19-Dec-26	2,725,882.92	1,864,255.11	100%	68.39%
FROM MH-12:MH-01		69	03-Aug-26	01-Nov-26	04-Nov-26 A	27-Jan-27	2,232,495.48	121,907.23	100%	5.46%
Sewage Network		58	03-Aug-26	13-Oct-26	22-Oct-26 A	02-Jan-27	651,749.20	421,026.21	100%	64.6%
FROM MH-18:MH-10		54	03-Aug-26	04-Oct-26	22-Oct-26 A	21-Nov-26	258,640.96	239,361.48	100%	92.55%
FROM MH-10:MH-01		40	17-Aug-26	13-Oct-26	04-Nov-26 A	02-Jan-27	393,108.24	181,664.73	100%	46.21%
Potable Water Network		42	14-Oct-26	23-Dec-26	21-Oct-26 A	08-Mar-27	956,108.40	92,554.02	50.07%	9.68%
Main Line Sections		13	14-Oct-26	10-Nov-26	21-Oct-26 A	17-Jan-27	522,248.40	92,554.02	91.67%	17.72%
Valve Chamber		16	11-Nov-26	29-Nov-26	17-Jan-27	04-Feb-27	259,440.00	0.00	0%	0%
Fire Hydrant		21	30-Nov-26	23-Dec-26	04-Feb-27	08-Mar-27	174,420.00	0.00	0%	0%
Irrigation Network		68	24-Oct-26	20-Dec-26	02-Jan-27	31-Mar-27	760,970.00	0.00	9.96%	0%
Main Line Pipes		68	24-Oct-26	20-Dec-26	02-Jan-27	31-Mar-27	760,970.00	0.00	9.96%	0%
Treated Sewage Effluent (Tse)		68	24-Oct-26	20-Dec-26	02-Jan-27	31-Mar-27	530,262.40	0.00	23.15%	0%
Main Line Pipes		68	24-Oct-26	20-Dec-26	02-Jan-27	31-Mar-27	530,262.40	0.00	23.15%	0%
Medium Voltage Network		43	02-Nov-26	21-Dec-26	04-Feb-27	05-Apr-27	639,985.36	0.00	2.96%	0%
Cabling Works		43	02-Nov-26	21-Dec-26	04-Feb-27	05-Apr-27	639,985.36	0.00	2.96%	0%
Street Lighting Network		67	02-Nov-26	18-Jan-27	04-Feb-27	03-May-27	824,676.69	0.00	2.27%	0%
Lighting Poles Works		35	02-Nov-26	12-Dec-26	04-Feb-27	27-Mar-27	239,640.00	0.00	7.81%	0%
Cabling Works		25	11-Nov-26	09-Dec-26	15-Feb-27	24-Mar-27	554,959.89	0.00	0%	0%
Distrubution Panel Boards		24	22-Dec-26	18-Jan-27	06-Apr-27	03-May-27	30,076.80	0.00	0%	0%
Telecom Network		42	15-Nov-26	02-Jan-27	20-Feb-27	17-Apr-27	4,775,135.00	0.00	0%	0%
Ducts Works		26	15-Nov-26	14-Dec-26	20-Feb-27	29-Mar-27	1,277,742.00	0.00	0%	0%
Manholes Works		19	24-Nov-26	15-Dec-26	04-Mar-27	30-Mar-27	266,796.00	0.00	0%	0%
CCTV System Wroks		15	16-Dec-26	02-Jan-27	31-Mar-27	17-Apr-27	3,230,597.00	0.00	0%	0%
Road Works		51	06-Dec-26	02-Feb-27	21-Mar-27	24-May-27	294,864.10	0.00	0%	0%
ST+1000:ST+1531		28	06-Dec-26	06-Jan-27	21-Mar-27	21-Apr-27	127,701.70	0.00	0%	0%
ST+500:ST+1000		25	22-Dec-26	19-Jan-27	06-Apr-27	04-May-27	78,701.70	0.00	0%	0%
ST+01:ST+500		26	03-Jan-27	02-Feb-27	18-Apr-27	24-May-27	88,460.70	0.00	0%	0%
Finishes for Infrastructure Networks		118	14-Oct-26	16-Feb-27	02-Jan-27	05-Jun-27	8,166,437.82	0.00	3.01%	0%
Storm Drainage Network		67	02-Nov-26	05-Jan-27	27-Jan-27	25-Apr-27	825,219.60	0.00	21.89%	0%
Sewage Network		41	14-Oct-26	13-Jan-27	02-Jan-27	22-Feb-27	85,302.80	0.00	76.69%	0%
Potable Water Network		43	24-Dec-26	28-Jan-27	08-Mar-27	29-Apr-27	83,407.60	0.00	0%	0%
Irrigation Network		12	21-Dec-26	03-Jan-27	01-Apr-27	14-Apr-27	19,320.00	0.00	0%	0%
Treated Sewage Effluent (Tse)		12	04-Jan-27	17-Jan-27	15-Apr-27	28-Apr-27	30,693.60	0.00	0%	0%
Medium Voltage Network		18	22-Dec-26	11-Jan-27	14-Apr-27	05-May-27	66,481.77	0.00	0%	0%
Street Lighting Network		14	12-Jan-27	03-Feb-27	27-Apr-27	12-May-27	143,686.20	0.00	0%	0%
Telecom Network		24	03-Jan-27	20-Jan-27	18-Apr-27	22-May-27	82,794.00	0.00	0%	0%
Road Works		47	21-Dec-26	16-Feb-27	05-Apr-27	05-Jun-27	6,829,532.25	0.00	0%	0%
Superstructure Work		245	28-Jul-26	23-Feb-27	28-Jul-26 A	26-May-27	39,833,640.35	18,761,903.47	45.88%	47.1%
Utility Buildings		216	24-Aug-26	28-Jan-27	01-Aug-26 A	26-May-27	14,839,553.75	2,683,926.91	16.34%	18.09%
Storm Drainage Ponds		63	22-Oct-26	03-Jan-27	02-Aug-26 A	01-Sep-26 A	446,400.00	446,400.00	0%	100%
Pump Station		216	01-Sep-26	28-Jan-27	01-Aug-26 A	26-May-27	4,089,766.36	1,057,254.27	14.91%	25.85%
Lift Station		125	10-Sep-26	21-Jan-27	01-Sep-26 A	26-Jan-27	2,816,702.49	504,484.04	18.96%	17.91%
Potable Water Tank		55	24-Aug-26	09-Nov-26	21-Oct-26 A	05-Jan-27	615,094.02	32,140.96	98.57%	5.23%
IrrigationTank		121	10-Nov-26	11-Jan-27	14-Oct-26 A	23-Dec-26	615,094.02	32,140.96	0%	5.23%
Control Room		111	17-Sep-26	21-Jan-27	02-Aug-26 A	23-Jan-27	2,330,956.41	611,506.69	28.32%	26.23%
Softscape and Planting Works		39	07-Nov-26	22-Dec-26	15-Mar-27	28-Apr-27	3,925,540.44	0.00	0.39%	0%
Fence and Gaurd Room		222	28-Jul-26	23-Feb-27	28-Jul-26 A	24-Apr-27	24,994,086.60	16,077,976.56	63.42%	64.33%
Gaurd Room Work		99	29-Aug-26	20-Jan-27	20-Oct-26 A	25-Mar-27	2,138,080.85	97,752.00	16.54%	4.57%
Fence Work		222	28-Jul-26	23-Feb-27	28-Jul-26 A	24-Apr-27	22,856,005.75	15,980,224.56	67.8%	69.92%
Testing and Comissioning		171	04-Jan-27	21-Feb-27	08-Nov-26	12-Jun-27	0.00	0.00	0%	0%
Infrastructure Networks		32	06-Jan-27	21-Feb-27	29-Apr-27	12-Jun-27	0.00	0.00	0%	0%
Irrigation Network		5	28-Jan-27	03-Feb-27	26-May-27	01-Jun-27	0.00	0.00	0%	0%
T/C-IR	Testing and Commissioning of Irrigation Network	5	28-Jan-27	03-Feb-27	26-May-27	01-Jun-27	0.00	0.00	0%	0%

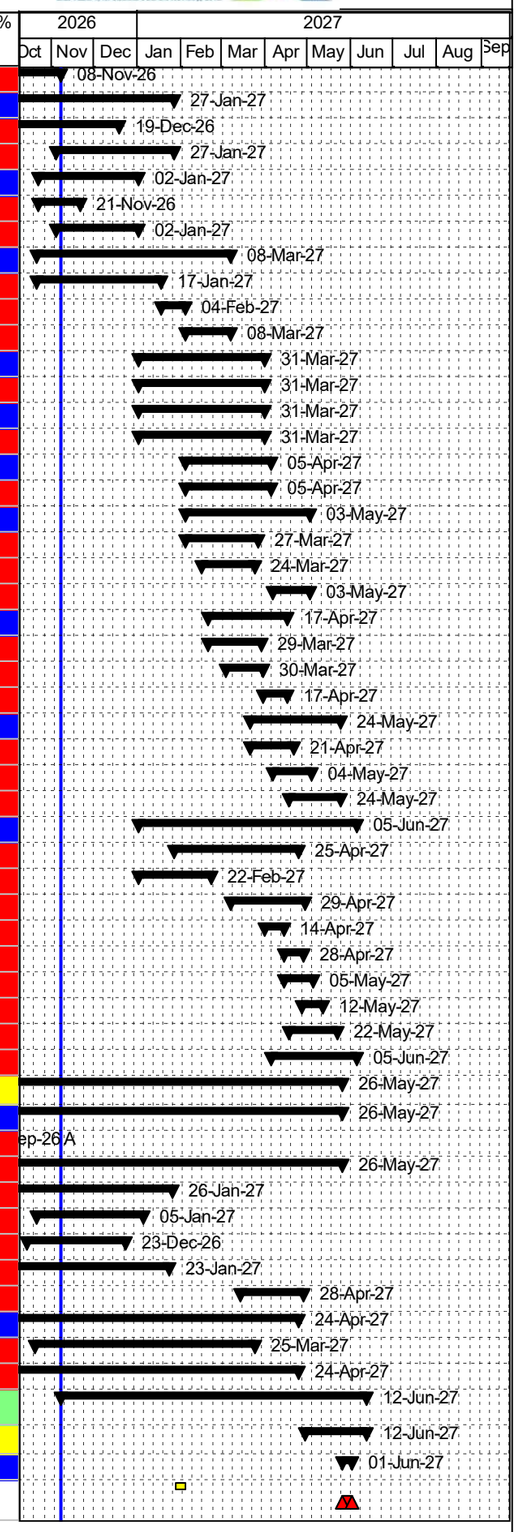


Primary Baseline | Actual Work | Summary
Remaining Work | Baseline Milestone
Critical Remaining Work | Milestone

Date	Revision	Checked	Approved
10-Nov-26	Third Industrial City		

Development of the Technology City in Dammam -Upda
10-11-2026
WPR UPS LEVEL 5

Activity ID	Activity Name	Original Duration	BL Project Start	BL Project Finish	Start	Finish	BL Project Total Cost	Earned Value Cost	Schedule % Complete	Performance % Complete
TSE Network		15	17-Jan-27	03-Feb-27	10-May-27	01-Jun-27	0.00	0.00	0%	0%
T/C-TSE-10	Testing and Commissioning of TSE Network	15	17-Jan-27	03-Feb-27	10-May-27	01-Jun-27	0.00	0.00	0%	0%
Potable Water Network		6	28-Jan-27	04-Feb-27	26-May-27	02-Jun-27	0.00	0.00	0%	0%
T/C-PW	Testing and Commissioning of Potable Water Network	6	28-Jan-27	04-Feb-27	26-May-27	02-Jun-27	0.00	0.00	0%	0%
Sewage Network		3	17-Jan-27	19-Jan-27	10-May-27	12-May-27	0.00	0.00	0%	0%
T/C-SW	Testing and Commissioning of Sewage Network	3	17-Jan-27	19-Jan-27	10-May-27	12-May-27	0.00	0.00	0%	0%
Storm Drainage Network		9	06-Jan-27	16-Jan-27	29-Apr-27	09-May-27	0.00	0.00	0%	0%
T/C-SD	Testing and Commissioning of Storm Drainage Network	9	06-Jan-27	16-Jan-27	29-Apr-27	09-May-27	0.00	0.00	0%	0%
Street Lighting Network		6	04-Feb-27	11-Feb-27	01-Jun-27	08-Jun-27	0.00	0.00	0%	0%
T/C-SL	Testing and Commissioning of Street Lighting Network	6	04-Feb-27	11-Feb-27	01-Jun-27	08-Jun-27	0.00	0.00	0%	0%
Telecom Network		3	21-Jan-27	24-Jan-27	22-May-27	25-May-27	0.00	0.00	0%	0%
T/C-TE	Testing and Commissioning of Telecom Network	3	21-Jan-27	24-Jan-27	22-May-27	25-May-27	0.00	0.00	0%	0%
Medium Voltage Network		14	21-Jan-27	06-Feb-27	22-May-27	07-Jun-27	0.00	0.00	0%	0%
T/C-MV	Testing and Commissioning of Medium Voltage Network	14	21-Jan-27	06-Feb-27	22-May-27	07-Jun-27	0.00	0.00	0%	0%
Road Works		4	15-Feb-27	21-Feb-27	07-Jun-27	12-Jun-27	0.00	0.00	0%	0%
T/C-RD	Testing and Commissioning of Road Works	4	15-Feb-27	21-Feb-27	07-Jun-27	12-Jun-27	0.00	0.00	0%	0%
Utility Buildings		163	04-Jan-27	03-Feb-27	08-Nov-26	02-Jun-27	0.00	0.00	0%	0%
T/C-CTV	Testing and Commissioning of Guard Room and Fence	0	23-Jan-27	23-Jan-27	27-Mar-27	27-Mar-27	0.00	0.00	0%	0%
T/C-SPS	Testing and Commissioning of Sewage Pump Stations& soft scape and planting work	0	03-Feb-27	03-Feb-27	02-Jun-27	02-Jun-27	0.00	0.00	0%	0%
T/C-DPO	Testing and Commissioning of Storm Drainage Ponds	0	04-Jan-27	04-Jan-27	08-Nov-26	08-Nov-26	0.00	0.00	0%	0%
Handing over and close out		179	04-Jan-27	24-Feb-27	08-Nov-26	21-Jun-27	0.00	0.00	0%	0%
As-Built		179	04-Jan-27	24-Feb-27	08-Nov-26	21-Jun-27	0.00	0.00	0%	0%
HO-190	As-Built Drawing For Potable Water Network	12	04-Feb-27	22-Feb-27	02-Jun-27	16-Jun-27	0.00	0.00	0%	0%
HO-180	Submission As-Built Drawing For Irrigation Network	12	03-Feb-27	21-Feb-27	01-Jun-27	15-Jun-27	0.00	0.00	0%	0%
HO-170	Submission As-Built Drawing For Medium Voltage Network	12	07-Feb-27	24-Feb-27	07-Jun-27	21-Jun-27	0.00	0.00	0%	0%
HO-130	Submission As-Built Drawing For Pond	14	04-Jan-27	19-Jan-27	08-Nov-26	23-Nov-26	0.00	0.00	0%	0%
HO-210	Submission As-Built Drawing For Pump station	1	03-Feb-27	04-Feb-27	02-Jun-27	02-Jun-27	0.00	0.00	0%	0%
HO-140	Submission As-Built Drawing For Roads Network	3	21-Feb-27	24-Feb-27	12-Jun-27	15-Jun-27	0.00	0.00	0%	0%
HO-100	Submission As-Built Drawing For Sewage Network	14	20-Jan-27	04-Feb-27	13-May-27	03-Jun-27	0.00	0.00	0%	0%
HO-150	Submission As-Built Drawing For Street Lighting Network	7	13-Feb-27	22-Feb-27	08-Jun-27	16-Jun-27	0.00	0.00	0%	0%
HO-160	Submission As-Built Drawing For Telecom Network	12	25-Jan-27	07-Feb-27	25-May-27	08-Jun-27	0.00	0.00	0%	0%
De-Mobilization Works		5	15-Feb-27	22-Feb-27	08-Jun-27	14-Jun-27	0.00	0.00	0%	0%
HO-230	Remove Temporary Car Shades	5	15-Feb-27	22-Feb-27	08-Jun-27	14-Jun-27	0.00	0.00	0%	0%
Handing Over		3	21-Feb-27	24-Feb-27	12-Jun-27	15-Jun-27	0.00	0.00	0%	0%
HO-250	Review B.O.Q Qty. to ensure compliance with the actual status	3	21-Feb-27	24-Feb-27	12-Jun-27	15-Jun-27	0.00	0.00	0%	0%

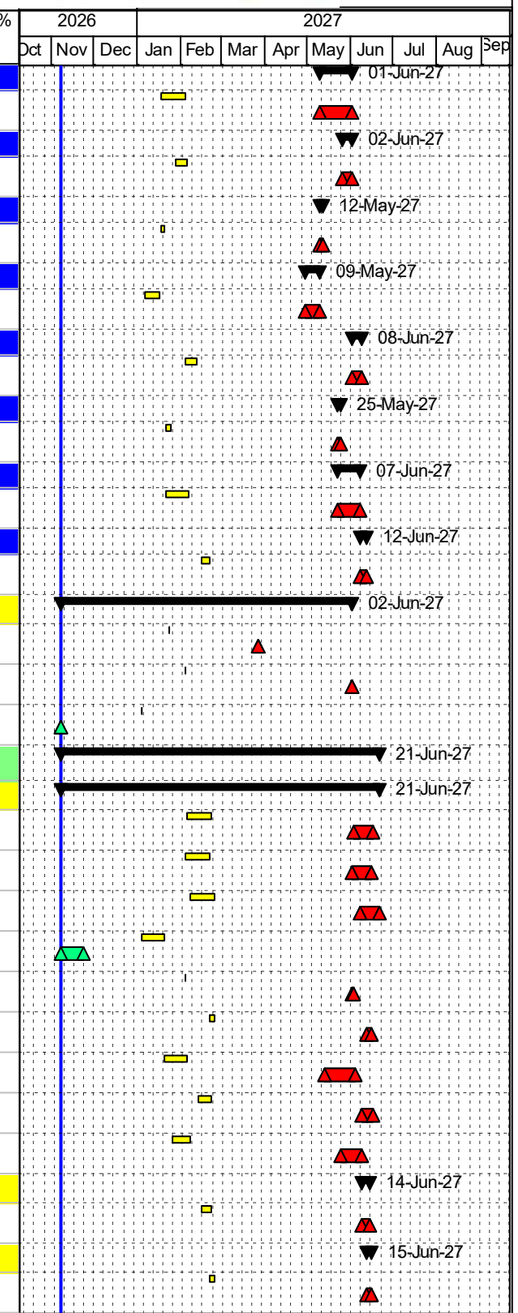

Primary Baseline
Remaining Work
Critical Remaining Work
Actual Work
Baseline Milestone
Milestone
Summary

Date	Revision	Checked	Approved
10-Nov-26	Third Industrial City		
