ENJAZCO


JDH1-02-003 - Infrastructure Development For Industrial City 1 In Jeddah - Update - 27.10.2026

Progress Tracker

egis

MODON

Activity ID	Activity Name	Original Duration	Budgeted Total Cost	BL Project Start	BL Project Finish	Actual Start	Actual Finish	Planned Value Cost	Earned Value Cost	Schedule Performance Index
JDH1-02-003 - Infrastructure Development For Industrial City 1 In Jeddah - Update -		769	86,782,344.73	19-Nov-25	18-Nov-27	19-Nov-25		46,518,471.52	69,295,883.48	1.49
Milestones		769	0.00	19-Nov-25	18-Nov-27	19-Nov-25		0.00	0.00	0.00
Key Milestones		769	0.00	19-Nov-25	18-Nov-27	19-Nov-25		0.00	0.00	0.00
CON-LEG101-MS-1090	Project Commencement Date	0	0.00	19-Nov-25		19-Nov-25		0.00	0.00	0.00
CON-LEG101-MS-1000	Project Completion Date	0	0.00		18-Nov-27			0.00	0.00	0.00
Contractual Milestone		739	0.00	18-Dec-25	18-Nov-27	18-Dec-25		0.00	0.00	0.00
Mobilization		0	0.00	18-Dec-25	18-Dec-25	04-Mar-26	04-Mar-26	0.00	0.00	0.00
CON-LEG101-MS-1070	Finish Mobilization	0	0.00		18-Dec-25		04-Mar-26	0.00	0.00	0.00
Time Schedule		0	0.00	18-Dec-25	18-Dec-25	18-Dec-25	18-Dec-25	0.00	0.00	0.00
CON-LEG101-MS-1080	Finish Baseline Time Schedule	0	0.00		18-Dec-25		18-Dec-25	0.00	0.00	0.00
Engineering		0	0.00	19-Jan-26	19-Jan-26			0.00	0.00	0.00
CON-LEG101-MS-1060	Finish Submission and Approval for Shop Drawings, Method of Stateme	0	0.00		19-Jan-26			0.00	0.00	0.00
Procurement		0	0.00	19-Jan-26	19-Jan-26			0.00	0.00	0.00
CON-LEG101-MS-1100	Finish PO for Short Lead Item & Long Lead Item	0	0.00		19-Jan-26			0.00	0.00	0.00
Construction		408	0.00	17-Sep-26	18-Nov-27			0.00	0.00	0.00
CON-LEG101-MS-1120	Completion of Roads & Meduim Voltage	0	0.00		17-Sep-26			0.00	0.00	0.00
CON-LEG101-MS-1130	Completion of Deep infrastructure network	0	0.00		18-Nov-26			0.00	0.00	0.00
CON-LEG101-MS-1140	Completion of Shallow infrastructure network	0	0.00		18-Mar-27			0.00	0.00	0.00
CON-LEG101-MS-1150	Completion all Works	0	0.00		18-Nov-27			0.00	0.00	0.00
Monitoring and Control Milestone		260	0.00	04-May-27	18-Oct-27			0.00	0.00	0.00
CON-LEG101-MS-1010	Completion of Roads Finishing	0	0.00		03-Aug-27			0.00	0.00	0.00
CON-LEG101-MS-1040	Completion of Fence and Gate	0	0.00		18-Oct-27			0.00	0.00	0.00
CON-LEG101-MS-1030	Completion of Roundabout & Landscape works	0	0.00		18-Oct-27			0.00	0.00	0.00
CON-LEG101-MS-1020	Completion of Bridge	0	0.00		01-Jun-27			0.00	0.00	0.00
CON-LEG101-MS-1050	Completion of Outside Boundary Area's Scope (Tie-in Lines)	0	0.00		04-May-27			0.00	0.00	0.00
Mobilization		112	0.00	19-Nov-25	18-Dec-25	19-Nov-25	04-Mar-26	0.00	0.00	0.00
Topographic Survey		8	0.00	19-Nov-25	27-Nov-25	19-Nov-25	27-Nov-25	0.00	0.00	0.00
CON-LEG101-TP-1330	Site Survey Works	8	0.00	19-Nov-25	27-Nov-25	19-Nov-25	27-Nov-25	0.00	0.00	0.00
Site Facilities & Offices		44	0.00	19-Nov-25	18-Dec-25	19-Nov-25	12-Jan-26	0.00	0.00	0.00
CON-LEG101-MB-1340	Site Layout Plan	6	0.00	19-Nov-25	25-Nov-25	19-Nov-25	25-Nov-25	0.00	0.00	0.00
CON-LEG101-MB-1270	Clear & Grub for Offices & Access Road	2	0.00	26-Nov-25	27-Nov-25	26-Nov-25	27-Nov-25	0.00	0.00	0.00
CON-LEG101-MB-1130	Install Site Facilities	7	0.00	07-Dec-25	14-Dec-25	26-Nov-25	27-Nov-25	0.00	0.00	0.00
CON-LEG101-MB-1260	Construct Site Access Roads	3	0.00	26-Nov-25	29-Nov-25	26-Nov-25	29-Nov-25	0.00	0.00	0.00
CON-LEG101-MB-1120	Electrical Works & Connections	11	0.00	07-Dec-25	18-Dec-25	26-Nov-25	29-Nov-25	0.00	0.00	0.00
CON-LEG101-MB-1000	Mobilization of Manpower	4	0.00	15-Dec-25	18-Dec-25	19-Nov-25	29-Nov-25	0.00	0.00	0.00
CON-LEG101-MB-1020	Mobilization of Equipment	6	0.00	13-Dec-25	18-Dec-25	19-Nov-25	29-Nov-25	0.00	0.00	0.00
CON-LEG101-MB-1250	Construct Temporary Fence	7	0.00	29-Nov-25	06-Dec-25	29-Nov-25	04-Dec-25	0.00	0.00	0.00
CON-LEG101-MB-1150	Install Project Signs	11	0.00	30-Nov-25	11-Dec-25	28-Dec-25	30-Dec-25	0.00	0.00	0.00
CON-LEG101-MB-1110	Construct Parking Sheds	11	0.00	07-Dec-25	18-Dec-25	28-Dec-25	06-Jan-26	0.00	0.00	0.00
CON-LEG101-MB-1160	Construct Site Offices & Storage	17	0.00	30-Nov-25	18-Dec-25	19-Nov-25	12-Jan-26	0.00	0.00	0.00
Permit's and Authority Approvals		47	0.00	19-Nov-25	09-Dec-25	19-Nov-25	20-Nov-25	0.00	0.00	0.00
CON-LEG101-PA-1000	Excavation & Backfilling Permit Permit	18	0.00	19-Nov-25	09-Dec-25	19-Nov-25	20-Nov-25	0.00	0.00	0.00
CON-LEG101-PA-1010	Saudi Electricity Company Permit	18	0.00	19-Nov-25	09-Dec-25	19-Nov-25	20-Nov-25	0.00	0.00	0.00
CON-LEG101-PA-1020	Utility Clearance (NOC) Permit	18	0.00	19-Nov-25	09-Dec-25	19-Nov-25	20-Nov-25	0.00	0.00	0.00
CON-LEG101-PA-1030	Landscaping & Irrigation Works Permit Permit	18	0.00	19-Nov-25	09-Dec-25	19-Nov-25	20-Nov-25	0.00	0.00	0.00
CON-LEG101-PA-1040	Material Transportation Permit (MOT)	18	0.00	19-Nov-25	09-Dec-25	19-Nov-25	20-Nov-25	0.00	0.00	0.00
Preliminary Submittals		112	0.00	19-Nov-25	18-Dec-25	19-Nov-25	04-Mar-26	0.00	0.00	0.00
Preparation and Submittal by Contractor's		37	0.00	19-Nov-25	11-Dec-25	19-Nov-25	28-Dec-25	0.00	0.00	0.00
CON-LEG101-PS-1070	Preparation and Submittal of Organization Chart	11	0.00	30-Nov-25	11-Dec-25	25-Nov-25	25-Nov-25	0.00	0.00	0.00
CON-LEG101-PS-1030	Preparation and Submittal of Safety Management Plan	11	0.00	30-Nov-25	11-Dec-25	10-Dec-25	10-Dec-25	0.00	0.00	0.00
CON-LEG101-PS-1050	Preparation and Submittal of Project Security Management Plan	11	0.00	30-Nov-25	11-Dec-25	10-Dec-25	10-Dec-25	0.00	0.00	0.00
CON-LEG101-PS-1040	Preparation and Submittal of Risk Plan	11	0.00	30-Nov-25	11-Dec-25	15-Dec-25	15-Dec-25	0.00	0.00	0.00

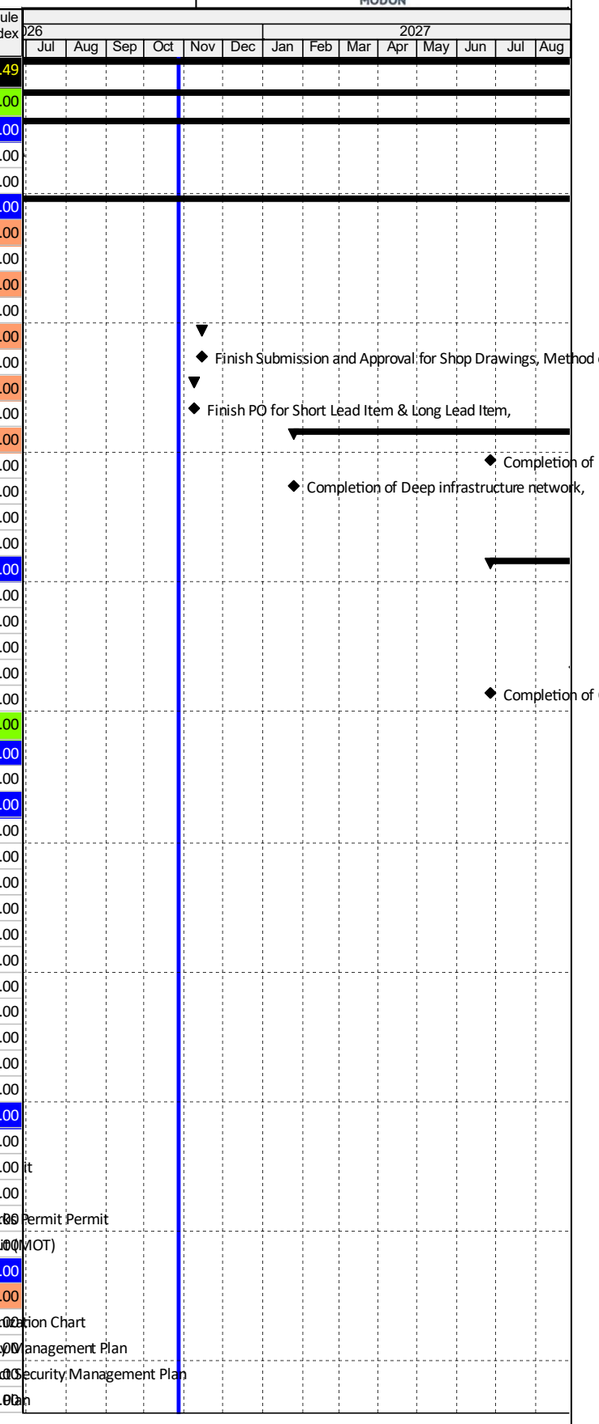


Actual Level of Effort | Actual Work | Critical Remaining Work
Primary Baseline | Remaining Work | Milestone

TASK filter: All Activities

© Oracle Corporation


27-Oct-26 08:23

Activity ID	Activity Name	Original Duration	Budgeted Total Cost	BL Project Start	BL Project Finish	Actual Start	Actual Finish	Planned Value Cost	Earned Value Cost	Schedule Performance Index
CON-LEG101-PS-1000	Preparation and Submittal of Detailed Work Order Programme (baselin	20	0.00	19-Nov-25	11-Dec-25	19-Nov-25	16-Dec-25	0.00	0.00	0.00
CON-LEG101-PS-1010	Preparation and Submittal of Project Execution Plan	11	0.00	30-Nov-25	11-Dec-25	25-Nov-25	27-Dec-25	0.00	0.00	0.00
CON-LEG101-PS-1060	Preparation and Submittal of Project Waste Management Plan	11	0.00	30-Nov-25	11-Dec-25	15-Dec-25	27-Dec-25	0.00	0.00	0.00
CON-LEG101-PS-1020	Preparation and Submittal of Quality Management Plan	11	0.00	30-Nov-25	11-Dec-25	25-Nov-25	28-Dec-25	0.00	0.00	0.00
Approval by the Employer's		88	0.00	30-Nov-25	18-Dec-25	17-Dec-25	04-Mar-26	0.00	0.00	0.00
CON-LEG101-PS-1090	Approval of Detailed Work Order Programme (baseline schedule)	6	0.00	13-Dec-25	18-Dec-25	17-Dec-25	18-Dec-25	0.00	0.00	0.00
CON-LEG101-PS-1130	Approval of Risk Plan	6	0.00	13-Dec-25	18-Dec-25	18-Dec-25	18-Dec-25	0.00	0.00	0.00
CON-LEG101-PS-1160	Approval of Organization Chart	6	0.00	13-Dec-25	18-Dec-25	08-Jan-26	08-Jan-26	0.00	0.00	0.00
CON-LEG101-PS-1170	Approval of Comminumcation Plan	6	0.00	30-Nov-25	06-Dec-25	15-Jan-26	15-Jan-26	0.00	0.00	0.00
CON-LEG101-PS-1140	Approval of Project Security Management Plan	6	0.00	13-Dec-25	18-Dec-25	03-Feb-26	03-Feb-26	0.00	0.00	0.00
CON-LEG101-PS-1150	Approval of Project Waste Management Plan	6	0.00	13-Dec-25	18-Dec-25	03-Feb-26	03-Feb-26	0.00	0.00	0.00
CON-LEG101-PS-1100	Approval of Project Execution Plan	6	0.00	13-Dec-25	18-Dec-25	05-Feb-26	05-Feb-26	0.00	0.00	0.00
CON-LEG101-PS-1110	Approval of Quality Management Plan	6	0.00	13-Dec-25	18-Dec-25	09-Feb-26	09-Feb-26	0.00	0.00	0.00
CON-LEG101-PS-1120	Approval of Safety Management Plan	6	0.00	13-Dec-25	18-Dec-25	03-Feb-26	04-Mar-26	0.00	0.00	0.00
Engineering		293	2,601,460.39	26-Nov-25	19-Jan-26	01-Dec-25		2,601,460.39	2,579,200.39	0.99
Shop Drawings		282	0.00	29-Nov-25	19-Jan-26	04-Dec-25		0.00	0.00	0.00
Shop Drawings Submittal		276	0.00	29-Nov-25	11-Jan-26	04-Dec-25		0.00	0.00	0.00
Shop Drawings Submittal for Stormwater Utilities		18	0.00	29-Nov-25	18-Dec-25	01-Jan-26	01-Jan-26	0.00	0.00	0.00
CON-LEG101-EN-1510	Shop DWG Submittal for Stormwater Utilities	9	0.00	29-Nov-25	08-Dec-25	01-Jan-26	01-Jan-26	0.00	0.00	0.00
CON-LEG101-EN-1520	Shop DWG Submittal for Stormwater Utilities Profiles	9	0.00	29-Nov-25	08-Dec-25	01-Jan-26	01-Jan-26	0.00	0.00	0.00
CON-LEG101-EN-1530	Shop DWG Submittal for Stormwater Utilities Standard Details	9	0.00	09-Dec-25	18-Dec-25	01-Jan-26	01-Jan-26	0.00	0.00	0.00
Shop Drawings Submittal for Sanitary Sewerage		9	0.00	09-Dec-25	18-Dec-25	16-Dec-25	16-Dec-25	0.00	0.00	0.00
CON-LEG101-EN-1480	Shop DWG Submittal for Sanitary Sewerage	9	0.00	09-Dec-25	18-Dec-25	16-Dec-25	16-Dec-25	0.00	0.00	0.00
CON-LEG101-EN-1490	Shop DWG Submittal for Sanitary Sewerage Profiles	9	0.00	09-Dec-25	18-Dec-25	16-Dec-25	16-Dec-25	0.00	0.00	0.00
CON-LEG101-EN-1500	Shop DWG Submittal for Sanitary Sewerage Standard Details	9	0.00	09-Dec-25	18-Dec-25	16-Dec-25	16-Dec-25	0.00	0.00	0.00
Shop Drawings Submittal for TSE Network		5	0.00	20-Dec-25	24-Dec-25	03-Jan-26	04-Jan-26	0.00	0.00	0.00
CON-LEG101-EN-1450	Shop DWG Submittal for TSE Network	5	0.00	20-Dec-25	24-Dec-25	03-Jan-26	04-Jan-26	0.00	0.00	0.00
CON-LEG101-EN-1460	Shop DWG Submittal for TSE Profiles	5	0.00	20-Dec-25	24-Dec-25	03-Jan-26	04-Jan-26	0.00	0.00	0.00
CON-LEG101-EN-1470	Shop DWG Submittal for TSE Standard Details	5	0.00	20-Dec-25	24-Dec-25	03-Jan-26	04-Jan-26	0.00	0.00	0.00
Shop Drawings Submittal for Public Water Utility Distribution		5	0.00	20-Dec-25	24-Dec-25	04-Jan-26	04-Jan-26	0.00	0.00	0.00
CON-LEG101-EN-1420	Shop DWG Submittal for Public Water Utility Distribution	5	0.00	20-Dec-25	24-Dec-25	04-Jan-26	04-Jan-26	0.00	0.00	0.00
CON-LEG101-EN-1430	Shop DWG Submittal for Potable Water Profiles	5	0.00	20-Dec-25	24-Dec-25	04-Jan-26	04-Jan-26	0.00	0.00	0.00
CON-LEG101-EN-1440	Shop DWG Submittal for Potable Water Standard Details	5	0.00	20-Dec-25	24-Dec-25	04-Jan-26	04-Jan-26	0.00	0.00	0.00
Shop Drawings Submittal for Electrical Network		256	0.00	25-Dec-25	04-Jan-26	17-Dec-25		0.00	0.00	0.00
CON-LEG101-EN-1410	Shop DWG Submittal for Low Voltage Network	9	0.00	25-Dec-25	04-Jan-26	17-Dec-25	17-Dec-25	0.00	0.00	0.00
CON-LEG101-EN-1400	Shop DWG Submittal for Street Lighting	9	0.00	25-Dec-25	04-Jan-26	18-Dec-25	18-Dec-25	0.00	0.00	0.00
CON-LEG101-EN-1390	Shop DWG Submittal for Medium Voltage Network	9	0.00	25-Dec-25	04-Jan-26			0.00	0.00	0.00
Shop Drawings Submittal for Telecommunications		9	0.00	25-Dec-25	04-Jan-26	17-Dec-25	17-Dec-25	0.00	0.00	0.00
CON-LEG101-EN-3190	Shop DWG Submittal for Telecommunications Works	9	0.00	25-Dec-25	04-Jan-26	17-Dec-25	17-Dec-25	0.00	0.00	0.00
Shop Drawings Submittal for CCTV feeding system and GSM		9	0.00	25-Dec-25	04-Jan-26	17-Dec-25	17-Dec-25	0.00	0.00	0.00
CON-LEG101-EN-3200	Shop DWG Submittal for CCTV feeding system and GSM	9	0.00	25-Dec-25	04-Jan-26	17-Dec-25	17-Dec-25	0.00	0.00	0.00
Shop Drawings Submittal for Earthing System		9	0.00	25-Dec-25	04-Jan-26	18-Dec-25	18-Dec-25	0.00	0.00	0.00
CON-LEG101-EN-3210	Shop DWG Submittal for Earthing System	9	0.00	25-Dec-25	04-Jan-26	18-Dec-25	18-Dec-25	0.00	0.00	0.00
Shop Drawings Submittal for Road Lighting		15	0.00	25-Dec-25	11-Jan-26	18-Dec-25	18-Dec-25	0.00	0.00	0.00
CON-LEG101-EN-1260	Shop DWG Submittal for Street Lighting General Arrangement	15	0.00	25-Dec-25	11-Jan-26	18-Dec-25	18-Dec-25	0.00	0.00	0.00
CON-LEG101-EN-1270	Shop DWG Submittal for Street Lighting Network Layout	15	0.00	25-Dec-25	11-Jan-26	18-Dec-25	18-Dec-25	0.00	0.00	0.00
CON-LEG101-EN-1280	Shop DWG Submittal for Street Lighting Details	15	0.00	25-Dec-25	11-Jan-26	18-Dec-25	18-Dec-25	0.00	0.00	0.00
CON-LEG101-EN-1290	Shop DWG Submittal for Street Lighting Single Line Diagram	15	0.00	25-Dec-25	11-Jan-26	18-Dec-25	18-Dec-25	0.00	0.00	0.00
Shop Drawings Submittal for Road Works		12	0.00	25-Dec-25	07-Jan-26	04-Dec-25	06-Dec-25	0.00	0.00	0.00
CON-LEG101-EN-1300	Shop DWG Submittal for Topographic Survey	6	0.00	25-Dec-25	31-Dec-25	04-Dec-25	06-Dec-25	0.00	0.00	0.00
CON-LEG101-EN-1310	Shop DWG Submittal for Road Layout Plan	6	0.00	01-Jan-26	07-Jan-26	04-Dec-25	06-Dec-25	0.00	0.00	0.00
CON-LEG101-EN-1320	Shop DWG Submittal for Typical Cross Section	6	0.00	01-Jan-26	07-Jan-26	04-Dec-25	06-Dec-25	0.00	0.00	0.00
CON-LEG101-EN-1330	Shop DWG Submittal for Road Setting Out	6	0.00	01-Jan-26	07-Jan-26	04-Dec-25	06-Dec-25	0.00	0.00	0.00

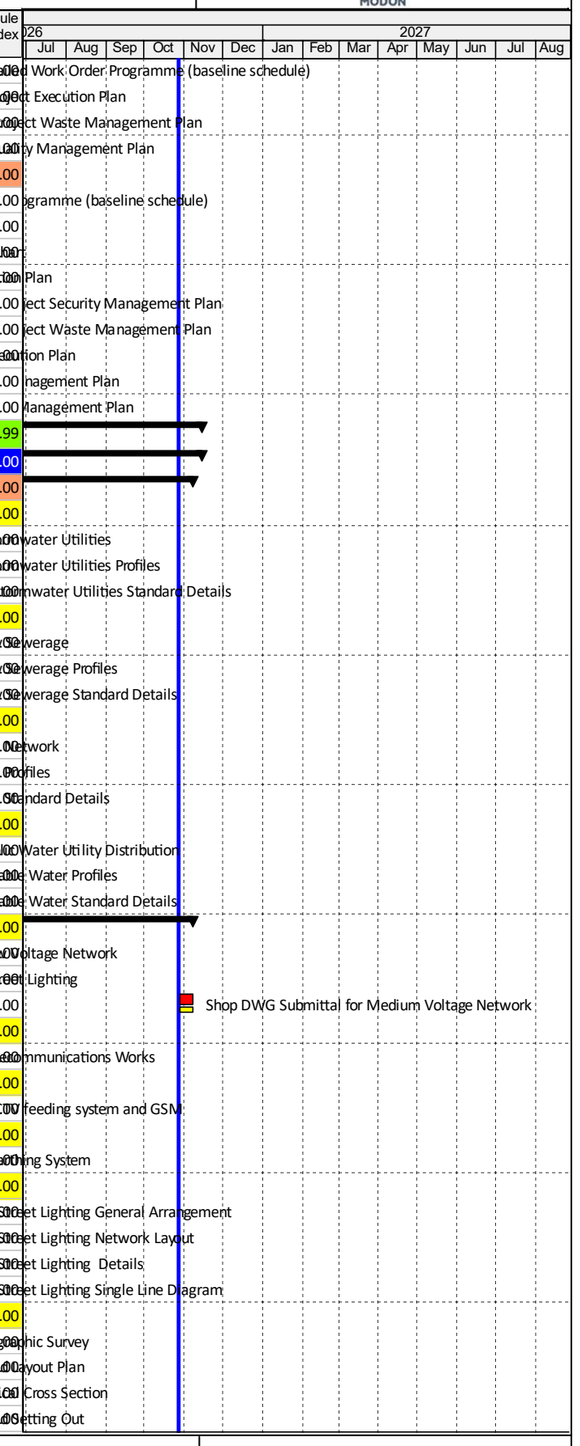


© Oracle Corporation

Activity ID	Activity Name	Original Duration	Budgeted Total Cost	BL Project Start	BL Project Finish	Actual Start	Actual Finish	Planned Value Cost	Earned Value Cost	Schedule Performance Index
CON-LEG101-EN-1340	Shop DWG Submittal for Road Profiles	6	0.00	01-Jan-26	07-Jan-26	04-Dec-25	06-Dec-25	0.00	0.00	0.00
Shop Drawings Submittal for Bridge Works		15	0.00	20-Dec-25	05-Jan-26	31-Dec-25	31-Dec-25	0.00	0.00	0.00
CON-LEG101-EN-1020	Shop DWG Submittal for Piles Setting out and Reinforcement Details	15	0.00	20-Dec-25	05-Jan-26	31-Dec-25	31-Dec-25	0.00	0.00	0.00
CON-LEG101-EN-1030	Shop DWG Submittal for Abutment Setting out and Reinforcement Deta	15	0.00	20-Dec-25	05-Jan-26	31-Dec-25	31-Dec-25	0.00	0.00	0.00
CON-LEG101-EN-1040	Shop DWG Submittal for Pier and Pilecap Setting out and Reinforcemer	15	0.00	20-Dec-25	05-Jan-26	31-Dec-25	31-Dec-25	0.00	0.00	0.00
CON-LEG101-EN-1060	Shop DWG Submittal for Deck Slab Setting out and Reinforcement Deta	15	0.00	20-Dec-25	05-Jan-26	31-Dec-25	31-Dec-25	0.00	0.00	0.00
CON-LEG101-EN-1070	Shop DWG Submittal for Bearing Setting out and Details	15	0.00	20-Dec-25	05-Jan-26	31-Dec-25	31-Dec-25	0.00	0.00	0.00
CON-LEG101-EN-1080	Shop DWG Submittal for Deflection Diagram	15	0.00	20-Dec-25	05-Jan-26	31-Dec-25	31-Dec-25	0.00	0.00	0.00
CON-LEG101-EN-1100	Shop DWG Submittal for Finishing Works Details	15	0.00	20-Dec-25	05-Jan-26	31-Dec-25	31-Dec-25	0.00	0.00	0.00
CON-LEG101-EN-1090	Shop DWG Submittal for Appron Slab Details	15	0.00	20-Dec-25	05-Jan-26	31-Dec-25	31-Dec-25	0.00	0.00	0.00
Shop Drawings Submittal for Irrigation Works		9	0.00	20-Dec-25	29-Dec-25	10-Jan-26	10-Jan-26	0.00	0.00	0.00
CON-LEG101-EN-3220	Shop DWG Submittal for Secondary Irrigation Pipe Works	9	0.00	20-Dec-25	29-Dec-25	10-Jan-26	10-Jan-26	0.00	0.00	0.00
CON-LEG101-EN-3230	Shop DWG Submittal for Secondary Irrigation Valves and Controller Wo	9	0.00	20-Dec-25	29-Dec-25	10-Jan-26	10-Jan-26	0.00	0.00	0.00
Shop Drawings Submittal for Landscape Works		9	0.00	20-Dec-25	29-Dec-25	10-Jan-26	10-Jan-26	0.00	0.00	0.00
CON-LEG101-EN-3240	Shop DWG Submittal for Preparation Works	9	0.00	20-Dec-25	29-Dec-25	10-Jan-26	10-Jan-26	0.00	0.00	0.00
CON-LEG101-EN-3250	Shop DWG Submittal for Placing Agricutural Soil works	9	0.00	20-Dec-25	29-Dec-25	10-Jan-26	10-Jan-26	0.00	0.00	0.00
CON-LEG101-EN-3260	Shop DWG Submittal for Planting Works	9	0.00	20-Dec-25	29-Dec-25	10-Jan-26	10-Jan-26	0.00	0.00	0.00
CON-LEG101-EN-3270	Shop DWG Submittal for Curb Setting Out Points	9	0.00	20-Dec-25	29-Dec-25	10-Jan-26	10-Jan-26	0.00	0.00	0.00
Shop Drawings Submittal for Fence & Gates		9	0.00	20-Dec-25	29-Dec-25	06-Dec-25	16-Dec-25	0.00	0.00	0.00
CON-LEG101-EN-1540	Shop DWG Submittal for the Fence & Gates - Civil Works	9	0.00	20-Dec-25	29-Dec-25	06-Dec-25	16-Dec-25	0.00	0.00	0.00
CON-LEG101-EN-1550	Shop DWG Submittal for the Fence & Gates - Mechanical Works	9	0.00	20-Dec-25	29-Dec-25	06-Dec-25	16-Dec-25	0.00	0.00	0.00
CON-LEG101-EN-1560	Shop DWG Submittal for the Fence & Gates - Finishing Works	9	0.00	20-Dec-25	29-Dec-25	06-Dec-25	16-Dec-25	0.00	0.00	0.00
Shop Drawings Approval		276	0.00	09-Dec-25	19-Jan-26	08-Dec-25		0.00	0.00	0.00
Shop Drawings Approval for Storm Network		18	0.00	09-Dec-25	29-Dec-25	07-Jan-26	03-Feb-26	0.00	0.00	0.00
CON-LEG101-EN-1780	Shop DWG Approval for Stormwater Utilities	6	0.00	09-Dec-25	15-Dec-25	07-Jan-26	03-Feb-26	0.00	0.00	0.00
CON-LEG101-EN-1790	Shop DWG Approval for Stormwater UtilitiesProfiles	6	0.00	16-Dec-25	22-Dec-25	07-Jan-26	03-Feb-26	0.00	0.00	0.00
CON-LEG101-EN-1800	Shop DWG Approval for Stormwater UtilitiesStandard Details	6	0.00	23-Dec-25	29-Dec-25	07-Jan-26	03-Feb-26	0.00	0.00	0.00
Shop Drawings Approval for Sanitary Sewerage		6	0.00	20-Dec-25	25-Dec-25	17-Dec-25	14-Jan-26	0.00	0.00	0.00
CON-LEG101-EN-1750	Shop DWG Approval for Sanitary Sewerage	6	0.00	20-Dec-25	25-Dec-25	17-Dec-25	14-Jan-26	0.00	0.00	0.00
CON-LEG101-EN-1760	Shop DWG Approval for Sanitary Sewerage Profiles	6	0.00	20-Dec-25	25-Dec-25	17-Dec-25	14-Jan-26	0.00	0.00	0.00
CON-LEG101-EN-1770	Shop DWG Approval for Sanitary Sewerage Standard Details	6	0.00	20-Dec-25	25-Dec-25	17-Dec-25	14-Jan-26	0.00	0.00	0.00
Shop Drawings Approval for TSE Network		6	0.00	25-Dec-25	31-Dec-25	08-Jan-26	20-Jan-26	0.00	0.00	0.00
CON-LEG101-EN-1720	Shop DWG Approval for TSE Network	6	0.00	25-Dec-25	31-Dec-25	08-Jan-26	20-Jan-26	0.00	0.00	0.00
CON-LEG101-EN-1730	Shop DWG Approval for TSE Profiles	6	0.00	25-Dec-25	31-Dec-25	08-Jan-26	20-Jan-26	0.00	0.00	0.00
CON-LEG101-EN-1740	Shop DWG Approval for TSE Standard Details	6	0.00	25-Dec-25	31-Dec-25	08-Jan-26	20-Jan-26	0.00	0.00	0.00
Shop Drawings Approval for Public Water Utility Distribution		6	0.00	25-Dec-25	31-Dec-25	10-Jan-26	15-Jan-26	0.00	0.00	0.00
CON-LEG101-EN-1690	Shop DWG Approval for Public Water Utility Distribution	6	0.00	25-Dec-25	31-Dec-25	10-Jan-26	15-Jan-26	0.00	0.00	0.00
CON-LEG101-EN-1700	Shop DWG Approval for Potable Water Profiles	6	0.00	25-Dec-25	31-Dec-25	10-Jan-26	15-Jan-26	0.00	0.00	0.00
CON-LEG101-EN-1710	Shop DWG Approval for Potable Water Standard Details	6	0.00	25-Dec-25	31-Dec-25	10-Jan-26	15-Jan-26	0.00	0.00	0.00
Shop Drawings Approval for Electrical Network		256	0.00	05-Jan-26	11-Jan-26	23-Dec-25		0.00	0.00	0.00
CON-LEG101-EN-1680	Shop DWG Approval for Low Voltage Network	6	0.00	05-Jan-26	11-Jan-26	23-Dec-25	23-Dec-25	0.00	0.00	0.00
CON-LEG101-EN-1670	Shop DWG Approval for Street Lighting	6	0.00	05-Jan-26	11-Jan-26	23-Dec-25	28-Feb-26	0.00	0.00	0.00
CON-LEG101-EN-1660	Shop DWG Approval for Medium Voltage Network	6	0.00	05-Jan-26	11-Jan-26			0.00	0.00	0.00
Shop Drawings Approval for Telecommunications		6	0.00	05-Jan-26	11-Jan-26	27-Dec-25	05-Apr-26	0.00	0.00	0.00
CON-LEG101-EN-3280	Shop DWG Approval for Telecommunications Works	6	0.00	05-Jan-26	11-Jan-26	27-Dec-25	05-Apr-26	0.00	0.00	0.00
Shop Drawings Approval for CCTV feeding system and GSM		6	0.00	05-Jan-26	11-Jan-26	14-Feb-26	14-Feb-26	0.00	0.00	0.00
CON-LEG101-EN-3290	Shop DWG Approval for CCTV feeding system and GSM	6	0.00	05-Jan-26	11-Jan-26	14-Feb-26	14-Feb-26	0.00	0.00	0.00
Shop Drawings Approval for Earthing System		6	0.00	05-Jan-26	11-Jan-26	23-Dec-25	23-Dec-25	0.00	0.00	0.00
CON-LEG101-EN-3300	Shop DWG Approval for Earthing System	6	0.00	05-Jan-26	11-Jan-26	23-Dec-25	23-Dec-25	0.00	0.00	0.00
Shop Drawings Approval for Road Lighting		6	0.00	29-Dec-25	04-Jan-26	23-Dec-25	28-Feb-26	0.00	0.00	0.00
CON-LEG101-EN-3310	Shop DWG Approval for Street Lighting General Arrangement	6	0.00	29-Dec-25	04-Jan-26	23-Dec-25	28-Feb-26	0.00	0.00	0.00
CON-LEG101-EN-3320	Shop DWG Approval for Street Lighting Network Layout	6	0.00	29-Dec-25	04-Jan-26	23-Dec-25	28-Feb-26	0.00	0.00	0.00
CON-LEG101-EN-3330	Shop DWG Approval for Street Lighting Details	6	0.00	29-Dec-25	04-Jan-26	23-Dec-25	28-Feb-26	0.00	0.00	0.00

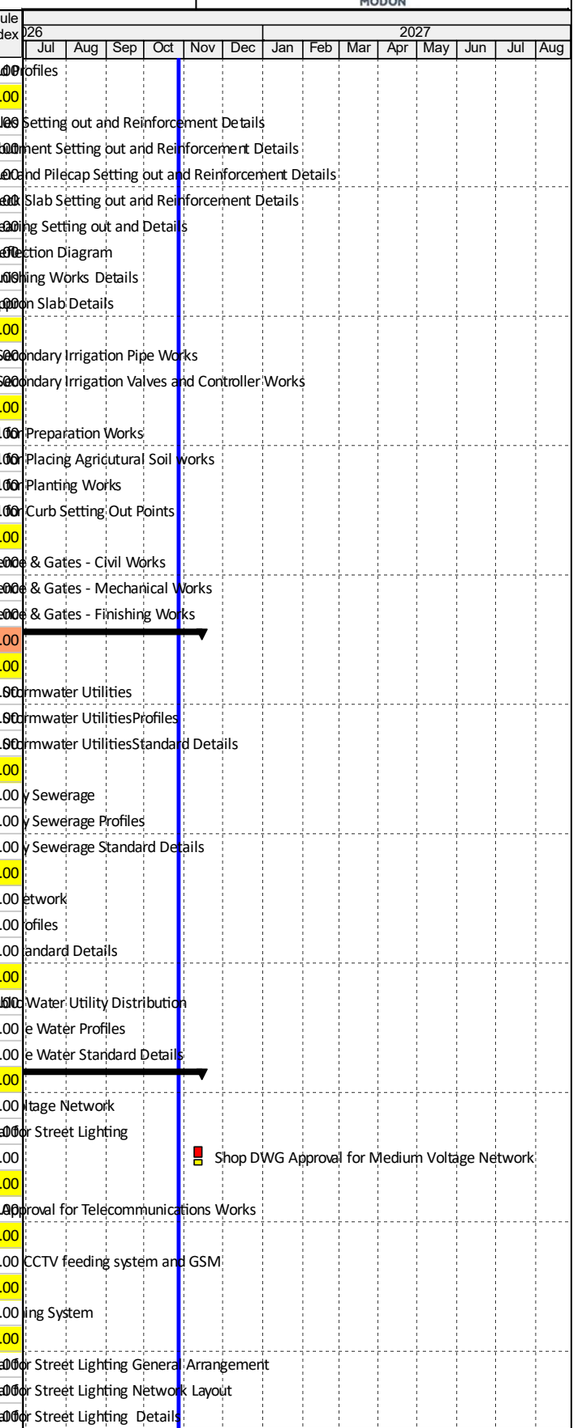


© Oracle Corporation

Activity ID	Activity Name	Original Duration	Budgeted Total Cost	BL Project Start	BL Project Finish	Actual Start	Actual Finish	Planned Value Cost	Earned Value Cost	Schedule Performance Index
CON-LEG101-EN-3360	Shop DWG Approval for Street Lighting Single Line Diagram	6	0.00	29-Dec-25	04-Jan-26	23-Dec-25	28-Feb-26	0.00	0.00	0.00
Shop Drawings Approval for Road Works		16	0.00	01-Jan-26	19-Jan-26	08-Dec-25	11-Jan-26	0.00	0.00	0.00
CON-LEG101-EN-1570	Shop DWG Approval for Topographic Survey	15	0.00	01-Jan-26	18-Jan-26	08-Dec-25	11-Jan-26	0.00	0.00	0.00
CON-LEG101-EN-1580	Shop DWG Approval for Road Layout Plan	10	0.00	08-Jan-26	19-Jan-26	08-Dec-25	11-Jan-26	0.00	0.00	0.00
CON-LEG101-EN-1590	Shop DWG Approval for Typical Cross Section	10	0.00	08-Jan-26	19-Jan-26	08-Dec-25	11-Jan-26	0.00	0.00	0.00
CON-LEG101-EN-1600	Shop DWG Approval for Road Setting Out	10	0.00	08-Jan-26	19-Jan-26	08-Dec-25	11-Jan-26	0.00	0.00	0.00
CON-LEG101-EN-1610	Shop DWG Approval for Road Profiles	10	0.00	08-Jan-26	19-Jan-26	08-Dec-25	11-Jan-26	0.00	0.00	0.00
Shop Drawings Approval for Bridge Works		18	0.00	06-Jan-26	19-Jan-26	11-Jan-26	20-Jan-26	0.00	0.00	0.00
CON-LEG101-EN-1150	Shop DWG Approval for Piles Setting out and Reinforcement Details	12	0.00	06-Jan-26	19-Jan-26	11-Jan-26	11-Jan-26	0.00	0.00	0.00
CON-LEG101-EN-1160	Shop DWG Approval for Abutment Setting out and Reinforcement Deta	12	0.00	06-Jan-26	19-Jan-26	11-Jan-26	11-Jan-26	0.00	0.00	0.00
CON-LEG101-EN-1170	Shop DWG Approval for Pier and Pilecap Setting out and Reinforcement	12	0.00	06-Jan-26	19-Jan-26	11-Jan-26	11-Jan-26	0.00	0.00	0.00
CON-LEG101-EN-1190	Shop DWG Approval for Deck Slab Setting out and Reinforcement Deta	12	0.00	06-Jan-26	19-Jan-26	11-Jan-26	11-Jan-26	0.00	0.00	0.00
CON-LEG101-EN-1200	Shop DWG Approval for Bearing Setting out and Details	12	0.00	06-Jan-26	19-Jan-26	11-Jan-26	11-Jan-26	0.00	0.00	0.00
CON-LEG101-EN-1210	Shop DWG Approval for Deflection Diagram	12	0.00	06-Jan-26	19-Jan-26	20-Jan-26	20-Jan-26	0.00	0.00	0.00
CON-LEG101-EN-1230	Shop DWG Approval for Finishing Works Details	12	0.00	06-Jan-26	19-Jan-26	20-Jan-26	20-Jan-26	0.00	0.00	0.00
CON-LEG101-EN-1220	Shop DWG Approval for Appron Slab Details	12	0.00	06-Jan-26	19-Jan-26	20-Jan-26	20-Jan-26	0.00	0.00	0.00
Shop Drawings Approval for Irrigation Works		6	0.00	30-Dec-25	05-Jan-26	15-Jan-26	15-Jan-26	0.00	0.00	0.00
CON-LEG101-EN-3340	Shop DWG Approval for Secondary Irrigation Pipe Works	6	0.00	30-Dec-25	05-Jan-26	15-Jan-26	15-Jan-26	0.00	0.00	0.00
CON-LEG101-EN-3350	Shop DWG Approval for Secondary Irrigation Valves and Controller Wor	6	0.00	30-Dec-25	05-Jan-26	15-Jan-26	15-Jan-26	0.00	0.00	0.00
Shop Drawings Approval for Landscape Works		9	0.00	30-Dec-25	08-Jan-26	14-Jan-26	08-Mar-26	0.00	0.00	0.00
CON-LEG101-EN-3370	Shop DWG Approval for Preparation Works	9	0.00	30-Dec-25	08-Jan-26	14-Jan-26	08-Mar-26	0.00	0.00	0.00
CON-LEG101-EN-3380	Shop DWG Approval for Placing Agricutural Soil works	9	0.00	30-Dec-25	08-Jan-26	14-Jan-26	08-Mar-26	0.00	0.00	0.00
CON-LEG101-EN-3390	Shop DWG Approval for Planting Works	9	0.00	30-Dec-25	08-Jan-26	14-Jan-26	08-Mar-26	0.00	0.00	0.00
CON-LEG101-EN-3400	Shop DWG Approval for Curb Setting Out Points	9	0.00	30-Dec-25	08-Jan-26	14-Jan-26	08-Mar-26	0.00	0.00	0.00
Shop Drawings Approval forFence & Gates		9	0.00	30-Dec-25	08-Jan-26	17-Dec-25	26-Jan-26	0.00	0.00	0.00
CON-LEG101-EN-3410	Shop DWG Approval for the Fence & Gates - Civil Works	9	0.00	30-Dec-25	08-Jan-26	17-Dec-25	26-Jan-26	0.00	0.00	0.00
CON-LEG101-EN-3420	Shop DWG Approval for the Fence & Gates - Mechanical Works	9	0.00	30-Dec-25	08-Jan-26	17-Dec-25	26-Jan-26	0.00	0.00	0.00
CON-LEG101-EN-3430	Shop DWG Approval for the Fence & Gates - Finishing Works	9	0.00	30-Dec-25	08-Jan-26	17-Dec-25	26-Jan-26	0.00	0.00	0.00
Method Statements		83	0.00	26-Nov-25	19-Jan-26	10-Dec-25	08-Feb-26	0.00	0.00	0.00
Method Statements Submittal		77	0.00	26-Nov-25	12-Jan-26	10-Dec-25	07-Feb-26	0.00	0.00	0.00
CON-LEG101-EN-1810	Preparation & Submission of Method Statement for Earth Works	14	0.00	26-Nov-25	11-Dec-25	10-Dec-25	10-Dec-25	0.00	0.00	0.00
CON-LEG101-EN-1820	Preparation & Submission of Method Statement for Concrete Works	14	0.00	30-Nov-25	15-Dec-25	20-Dec-25	20-Dec-25	0.00	0.00	0.00
CON-LEG101-EN-1830	Preparation & Submission of Method Statement for Waterproofing Wor	14	0.00	03-Dec-25	18-Dec-25	23-Dec-25	23-Dec-25	0.00	0.00	0.00
CON-LEG101-EN-1840	Preparation & Submission of Method Statement for Asphalt	14	0.00	20-Dec-25	04-Jan-26	23-Dec-25	23-Dec-25	0.00	0.00	0.00
CON-LEG101-EN-1860	Preparation & Submission of Method Statement for Storm Network	14	0.00	30-Nov-25	15-Dec-25	27-Dec-25	27-Dec-25	0.00	0.00	0.00
CON-LEG101-EN-1870	Preparation & Submission of Method Statement for Sewer Network	14	0.00	30-Nov-25	15-Dec-25	28-Dec-25	28-Dec-25	0.00	0.00	0.00
CON-LEG101-EN-1880	Preparation & Submission of Method Statement for Potable Water Netv	14	0.00	03-Dec-25	18-Dec-25	28-Dec-25	28-Dec-25	0.00	0.00	0.00
CON-LEG101-EN-1950	Preparation & Submission of Method Statement for Bridge Slabs	14	0.00	15-Dec-25	30-Dec-25	29-Dec-25	29-Dec-25	0.00	0.00	0.00
CON-LEG101-EN-1940	Preparation & Submission of Method Statement for Girders & Post Tens	14	0.00	11-Dec-25	27-Dec-25	30-Dec-25	30-Dec-25	0.00	0.00	0.00
CON-LEG101-EN-1930	Preparation & Submission of Method Statement for Piles of Bridge	14	0.00	08-Dec-25	23-Dec-25	03-Jan-26	03-Jan-26	0.00	0.00	0.00
CON-LEG101-EN-1850	Preparation & Submission of Method Statement for Paving	14	0.00	28-Dec-25	12-Jan-26	04-Jan-26	04-Jan-26	0.00	0.00	0.00
CON-LEG101-EN-1890	Preparation & Submission of Method Statement for TSE Network	14	0.00	07-Dec-25	22-Dec-25	14-Jan-26	14-Jan-26	0.00	0.00	0.00
CON-LEG101-EN-1920	Preparation & Submission of Method Statement for Telecome System	14	0.00	14-Dec-25	29-Dec-25	15-Jan-26	15-Jan-26	0.00	0.00	0.00
CON-LEG101-EN-1960	Preparation & Submission of Method Statement for Fence and Gates	14	0.00	16-Dec-25	31-Dec-25	20-Dec-25	19-Jan-26	0.00	0.00	0.00
CON-LEG101-EN-1900	Preparation & Submission of Method Statement for Electrical System	14	0.00	10-Dec-25	25-Dec-25	08-Jan-26	25-Jan-26	0.00	0.00	0.00
CON-LEG101-EN-1910	Preparation & Submission of Method Statement for Low Current Systen	14	0.00	14-Dec-25	29-Dec-25	07-Feb-26	07-Feb-26	0.00	0.00	0.00
Method Statements Approval		60	0.00	13-Dec-25	19-Jan-26	20-Dec-25	08-Feb-26	0.00	0.00	0.00
CON-LEG101-EN-3440	Approval of Method Statement for Earth Works	6	0.00	13-Dec-25	18-Dec-25	20-Dec-25	20-Dec-25	0.00	0.00	0.00
CON-LEG101-EN-3460	Approval of Method Statement for Waterproofing Works	6	0.00	30-Dec-25	05-Jan-26	27-Dec-25	27-Dec-25	0.00	0.00	0.00
CON-LEG101-EN-3450	Approval of Method Statement for Concrete Works	6	0.00	20-Dec-25	25-Dec-25	28-Dec-25	04-Jan-26	0.00	0.00	0.00
CON-LEG101-EN-3560	Approval of Method Statement for Piles of Bridge	6	0.00	24-Dec-25	30-Dec-25	04-Jan-26	04-Jan-26	0.00	0.00	0.00
CON-LEG101-EN-3570	Approval of Method Statement for Girders & Post Tension	6	0.00	28-Dec-25	03-Jan-26	04-Jan-26	04-Jan-26	0.00	0.00	0.00
CON-LEG101-EN-3580	Approval of Method Statement for Bridge Slabs	6	0.00	31-Dec-25	06-Jan-26	04-Jan-26	04-Jan-26	0.00	0.00	0.00

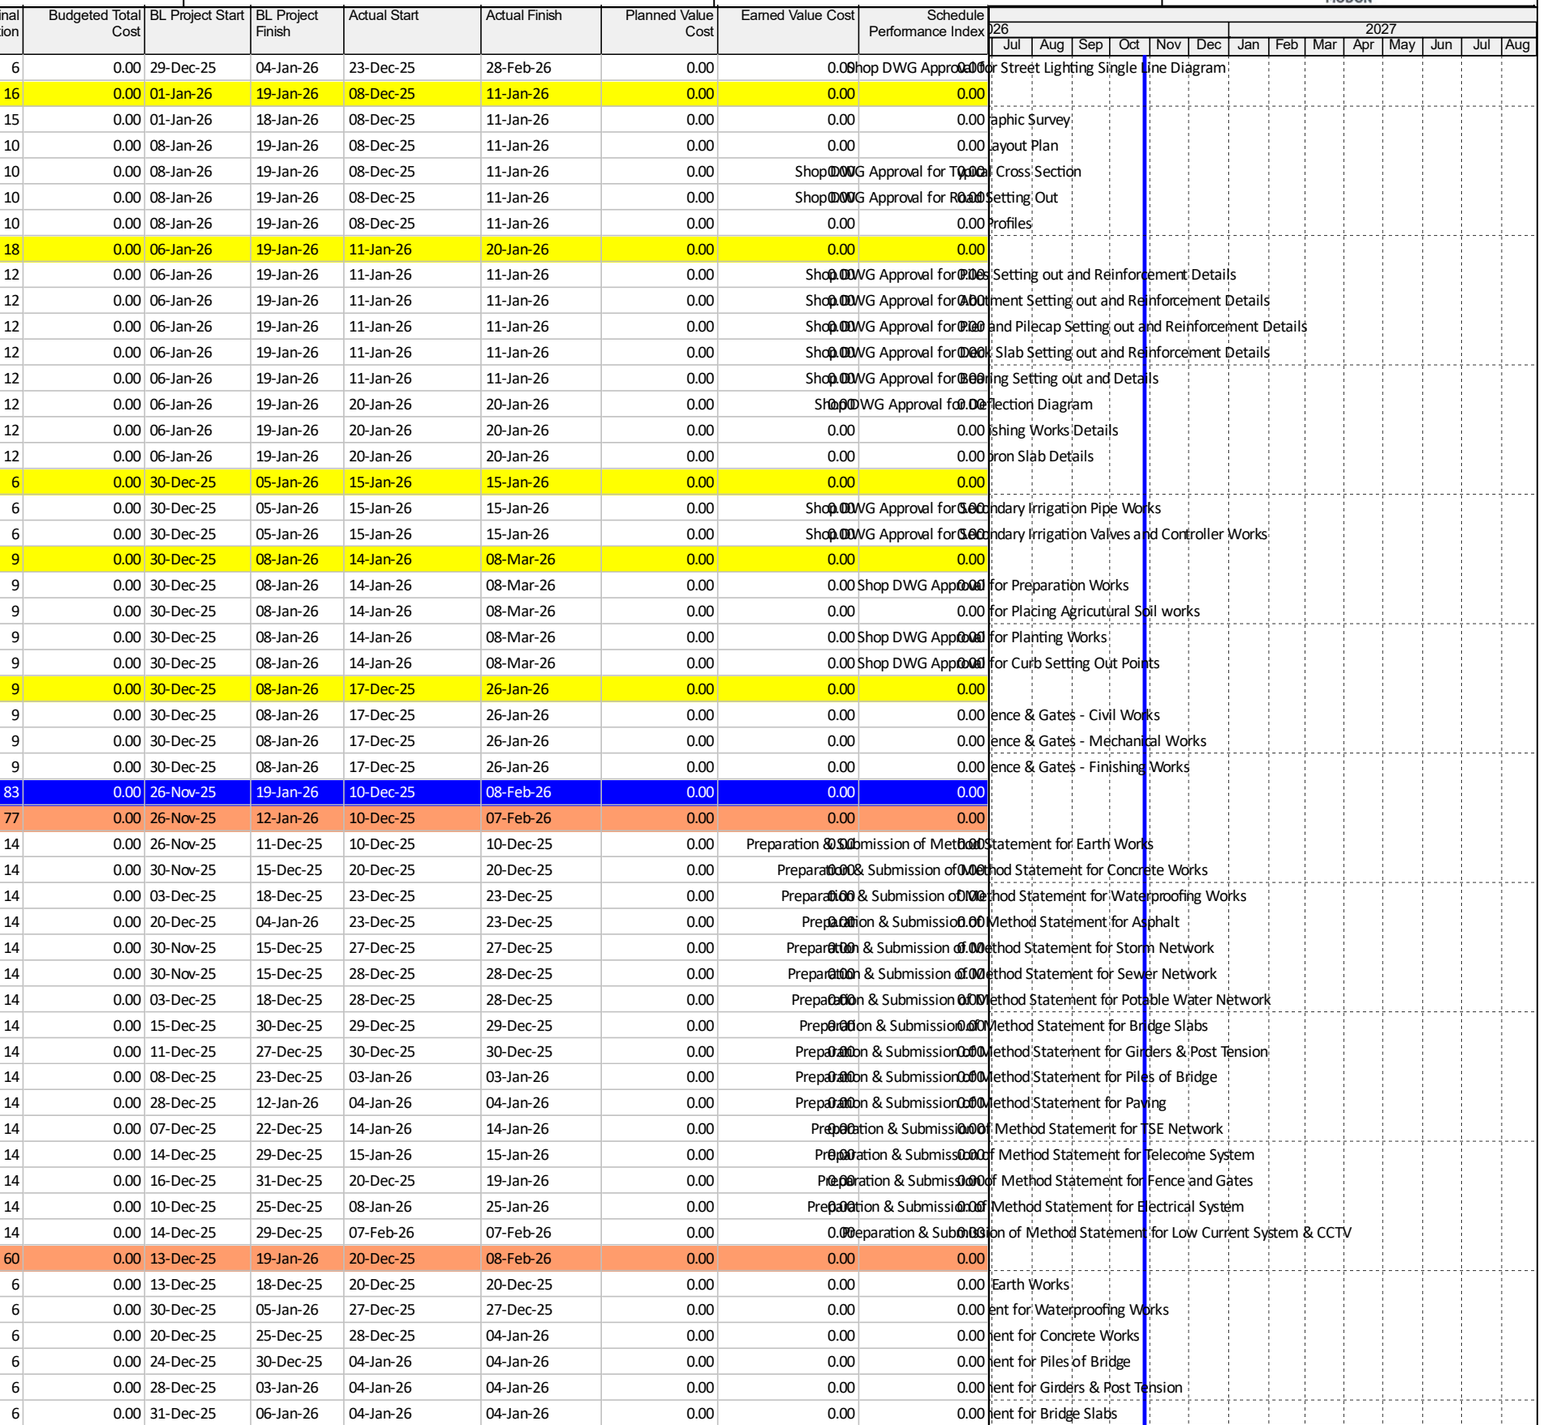


© Oracle Corporation

Activity ID	Activity Name	Original Duration	Budgeted Total Cost	BL Project Start	BL Project Finish	Actual Start	Actual Finish	Planned Value Cost	Earned Value Cost	Schedule Performance Index
CON-LEG101-EN-3470	Approval of Method Statement for Asphalt	6	0.00	05-Jan-26	11-Jan-26	11-Jan-26	11-Jan-26	0.00	0.00	0.00
CON-LEG101-EN-3490	Approval of Method Statement for Storm Network	6	0.00	06-Jan-26	12-Jan-26	04-Jan-26	11-Jan-26	0.00	0.00	0.00
CON-LEG101-EN-3530	Approval of Method Statement for Electrical System	6	0.00	27-Dec-25	01-Jan-26	11-Jan-26	11-Jan-26	0.00	0.00	0.00
CON-LEG101-EN-3480	Approval of Method Statement for Paving	6	0.00	13-Jan-26	19-Jan-26	13-Jan-26	13-Jan-26	0.00	0.00	0.00
CON-LEG101-EN-3500	Approval of Method Statement for Sewer Network	6	0.00	16-Dec-25	22-Dec-25	14-Jan-26	17-Jan-26	0.00	0.00	0.00
CON-LEG101-EN-3520	Approval of Method Statement for TSE Network	6	0.00	06-Jan-26	12-Jan-26	17-Jan-26	17-Jan-26	0.00	0.00	0.00
CON-LEG101-EN-3550	Approval of Method Statement for Telecome System	6	0.00	30-Dec-25	05-Jan-26	17-Jan-26	17-Jan-26	0.00	0.00	0.00
CON-LEG101-EN-3510	Approval of Method Statement for Potable Water Network	6	0.00	23-Dec-25	29-Dec-25	27-Jan-26	27-Jan-26	0.00	0.00	0.00
CON-LEG101-EN-3590	Approval of Method Statement for Fence and Gates	6	0.00	01-Jan-26	07-Jan-26	05-Feb-26	05-Feb-26	0.00	0.00	0.00
CON-LEG101-EN-3540	Approval of Method Statement for Low Current System & CCTV	6	0.00	30-Dec-25	05-Jan-26	08-Feb-26	08-Feb-26	0.00	0.00	0.00
Pre-qualification and Material		90	2,601,460.39	15-Dec-25	19-Jan-26	01-Dec-25		2,601,460.39	2,579,200.39	0.99
Road Works - Civil		44	795,816.59	15-Dec-25	11-Jan-26	01-Dec-25	24-Jan-26	795,816.59	795,816.59	1.00
Steel Reinforcement		11	2,262.75	15-Dec-25	27-Dec-25	08-Dec-25	14-Dec-25	2,262.75	2,262.75	1.00
CON-LEG101-SB-4260	Pre-qualification and Material Submittal for Steel Reinforcement	5	0.00	15-Dec-25	20-Dec-25	08-Dec-25	08-Dec-25	0.00	Pre-qualification and Material Submittal for Steel Reinforcement	0.00
CON-LEG101-SB-4270	Pre-qualification and Material Approval for Steel Reinforcement	6	2,262.75	21-Dec-25	27-Dec-25	09-Dec-25	14-Dec-25	2,262.75	Pre-qualification and Material Approval for Steel Reinforcement	1.00
Ready Mixed Concrete		28	10,272.00	21-Dec-25	30-Dec-25	01-Dec-25	01-Jan-26	10,272.00	10,272.00	1.00
CON-LEG101-SB-4280	Pre-qualification and Material Submittal for Ready Mixed Concrete	3	0.00	21-Dec-25	23-Dec-25	01-Dec-25	16-Dec-25	0.00	Pre-qualification and Material Submittal for Ready Mixed Concrete	0.00
CON-LEG101-SB-4290	Pre-qualification and Material Approval for Ready Mixed Concrete	6	10,272.00	24-Dec-25	30-Dec-25	01-Jan-26	01-Jan-26	10,272.00	Pre-qualification and Material Approval for Ready Mixed Concrete	1.00
Water Proofing		16	0.00	24-Dec-25	05-Jan-26	16-Dec-25	24-Jan-26	0.00	0.00	0.00
CON-LEG101-SB-4300	Pre-qualification and Material Submittal for Water Proofing	5	0.00	24-Dec-25	29-Dec-25	16-Dec-25	06-Jan-26	0.00	Pre-qualification and Material Submittal for Water Proofing	0.00
CON-LEG101-SB-4310	Pre-qualification and Material Approval for Water Proofing	6	0.00	30-Dec-25	05-Jan-26	21-Dec-25	24-Jan-26	0.00	Pre-qualification and Material Approval for Water Proofing	0.00
Aggregate Base Course		11	272,384.84	24-Dec-25	05-Jan-26	01-Dec-25	13-Jan-26	272,384.84	272,384.84	1.00
CON-LEG101-SB-1020	Pre-qualification and Material Submittal for Aggregate Base Cource	5	0.00	24-Dec-25	29-Dec-25	01-Dec-25	13-Jan-26	0.00	Pre-qualification and Material Submittal for Aggregate Base Cource	0.00
CON-LEG101-SB-1030	Pre-qualification and Material Approval for Aggregate Base Cource	6	272,384.84	30-Dec-25	05-Jan-26	02-Dec-25	13-Jan-26	272,384.84	Pre-qualification and Material Approval for Aggregate Base Cource	1.00
Bituminous Base & Wearing Course		11	250,806.00	30-Dec-25	11-Jan-26	01-Dec-25	13-Jan-26	250,806.00	250,806.00	1.00
CON-LEG101-SB-1060	Pre-qualification and Material Submittal for Bituminous Base & Wearin	5	0.00	30-Dec-25	04-Jan-26	01-Dec-25	13-Jan-26	0.00	Pre-qualification and Material Submittal for Bituminous Base & Wearing Cource	0.00
CON-LEG101-SB-1070	Pre-qualification and Material Approval for Bituminous Base & Wearing	6	250,806.00	05-Jan-26	11-Jan-26	02-Dec-25	13-Jan-26	250,806.00	Pre-qualification and Material Approval for Bituminous Base & Wearing Cource	1.00
Precast Concrete Kerb		7	101,523.00	30-Dec-25	11-Jan-26	16-Dec-25	24-Jan-26	101,523.00	101,523.00	1.00
CON-LEG101-SB-1100	Pre-qualification and Material Submittal for Precast Concrete Kerb	5	0.00	30-Dec-25	04-Jan-26	16-Dec-25	17-Jan-26	0.00	Pre-qualification and Material Submittal for Precast Concrete Kerb	0.00
CON-LEG101-SB-1110	Pre-qualification and Material Approval for Precast Concrete Kerb	6	101,523.00	05-Jan-26	11-Jan-26	18-Dec-25	24-Jan-26	101,523.00	Pre-qualification and Material Approval for Precast Concrete Kerb	1.00
Interlocking Block Pavers		7	127,386.00	30-Dec-25	11-Jan-26	16-Dec-25	24-Jan-26	127,386.00	127,386.00	1.00
CON-LEG101-SB-1140	Pre-qualification and Material Submittal for Interlocking Block Pavers	5	0.00	30-Dec-25	04-Jan-26	16-Dec-25	17-Jan-26	0.00	Pre-qualification and Material Submittal for Interlocking Block Pavers	0.00
CON-LEG101-SB-1150	Pre-qualification and Material Approval for Interlocking Block Pavers	6	127,386.00	05-Jan-26	11-Jan-26	18-Dec-25	24-Jan-26	127,386.00	Pre-qualification and Material Approval for Interlocking Block Pavers	1.00
Pavement Markings		15	5,373.00	30-Dec-25	11-Jan-26	07-Jan-26	18-Jan-26	5,373.00	5,373.00	1.00
CON-LEG101-SB-1190	Pre-qualification and Material Approval for Pavement Markings	6	5,373.00	05-Jan-26	11-Jan-26	13-Jan-26	18-Jan-26	5,373.00	Pre-qualification and Material Approval for Pavement Markings	1.00
CON-LEG101-SB-1180	Pre-qualification and Material Submittal for Pavement Markings	5	0.00	30-Dec-25	04-Jan-26	07-Jan-26	18-Jan-26	0.00	Pre-qualification and Material Submittal for Pavement Markings	0.00
Handicap ramp		18	5,220.00	30-Dec-25	11-Jan-26	07-Jan-26	18-Jan-26	5,220.00	5,220.00	1.00
CON-LEG101-SB-2130	Pre-qualification and Material Submittal for Handicap ramp	5	0.00	30-Dec-25	04-Jan-26	07-Jan-26	17-Jan-26	0.00	Pre-qualification and Material Submittal for Handicap ramp	0.00
CON-LEG101-SB-2370	Pre-qualification and Material Approval for Handicap ramp	6	5,220.00	05-Jan-26	11-Jan-26	18-Jan-26	18-Jan-26	5,220.00	Pre-qualification and Material Approval for Handicap ramp	1.00
Traffic Signs		13	20,589.00	30-Dec-25	11-Jan-26	14-Jan-26	24-Jan-26	20,589.00	20,589.00	1.00
CON-LEG101-SB-1220	Pre-qualification and Material Submittal for Traffic Signs	5	0.00	30-Dec-25	04-Jan-26	14-Jan-26	21-Jan-26	0.00	Pre-qualification and Material Submittal for Traffic Signs	0.00
CON-LEG101-SB-1230	Pre-qualification and Material Approval for Traffic Signs	6	20,589.00	05-Jan-26	11-Jan-26	24-Jan-26	24-Jan-26	20,589.00	Pre-qualification and Material Approval for Traffic Signs	1.00
Stormwater Utilities		24	312,469.80	16-Dec-25	12-Jan-26	11-Dec-25	28-Jan-26	312,469.80	312,469.80	1.00
GRP Pipes		13	141,529.50	16-Dec-25	30-Dec-25	11-Dec-25	21-Dec-25	141,529.50	141,529.50	1.00
CON-LEG101-SB-1580	Pre-qualification and Material Submittal for GRP Pipe	7	0.00	16-Dec-25	23-Dec-25	11-Dec-25	11-Dec-25	0.00	Pre-qualification and Material Submittal for GRP Pipe	0.00
CON-LEG101-SB-1590	Pre-qualification and Material Approval for GRP Pipe	6	141,529.50	24-Dec-25	30-Dec-25	11-Dec-25	21-Dec-25	141,529.50	Pre-qualification and Material Approval for GRP Pipe	1.00
Inlet Manholes		10	73,365.00	24-Dec-25	04-Jan-26	11-Dec-25	22-Dec-25	73,365.00	73,365.00	1.00
CON-LEG101-SB-3320	Pre-qualification and Material Submittal for Inlet Manholes	4	0.00	24-Dec-25	28-Dec-25	11-Dec-25	21-Dec-25	0.00	Pre-qualification and Material Submittal for Inlet Manholes	0.00
CON-LEG101-SB-3330	Pre-qualification and Material Approval for Inlet Manholes	6	73,365.00	29-Dec-25	04-Jan-26	11-Dec-25	22-Dec-25	73,365.00	Pre-qualification and Material Approval for Inlet Manholes	1.00
UPVC Pipes		12	45,585.30	16-Dec-25	29-Dec-25	11-Dec-25	28-Jan-26	45,585.30	45,585.30	1.00
CON-LEG101-SB-1540	Pre-qualification and Material Submittal for UPVC Pipes	6	0.00	16-Dec-25	22-Dec-25	11-Dec-25	11-Jan-26	0.00	Pre-qualification and Material Submittal for UPVC Pipes	0.00
CON-LEG101-SB-1550	Pre-qualification and Material Approval for UPVC Pipes	6	45,585.30	23-Dec-25	29-Dec-25	11-Dec-25	28-Jan-26	45,585.30	Pre-qualification and Material Approval for UPVC Pipes	1.00
Concrete chambers		13	51,990.00	29-Dec-25	12-Jan-26	11-Dec-25	22-Dec-25	51,990.00	51,990.00	1.00

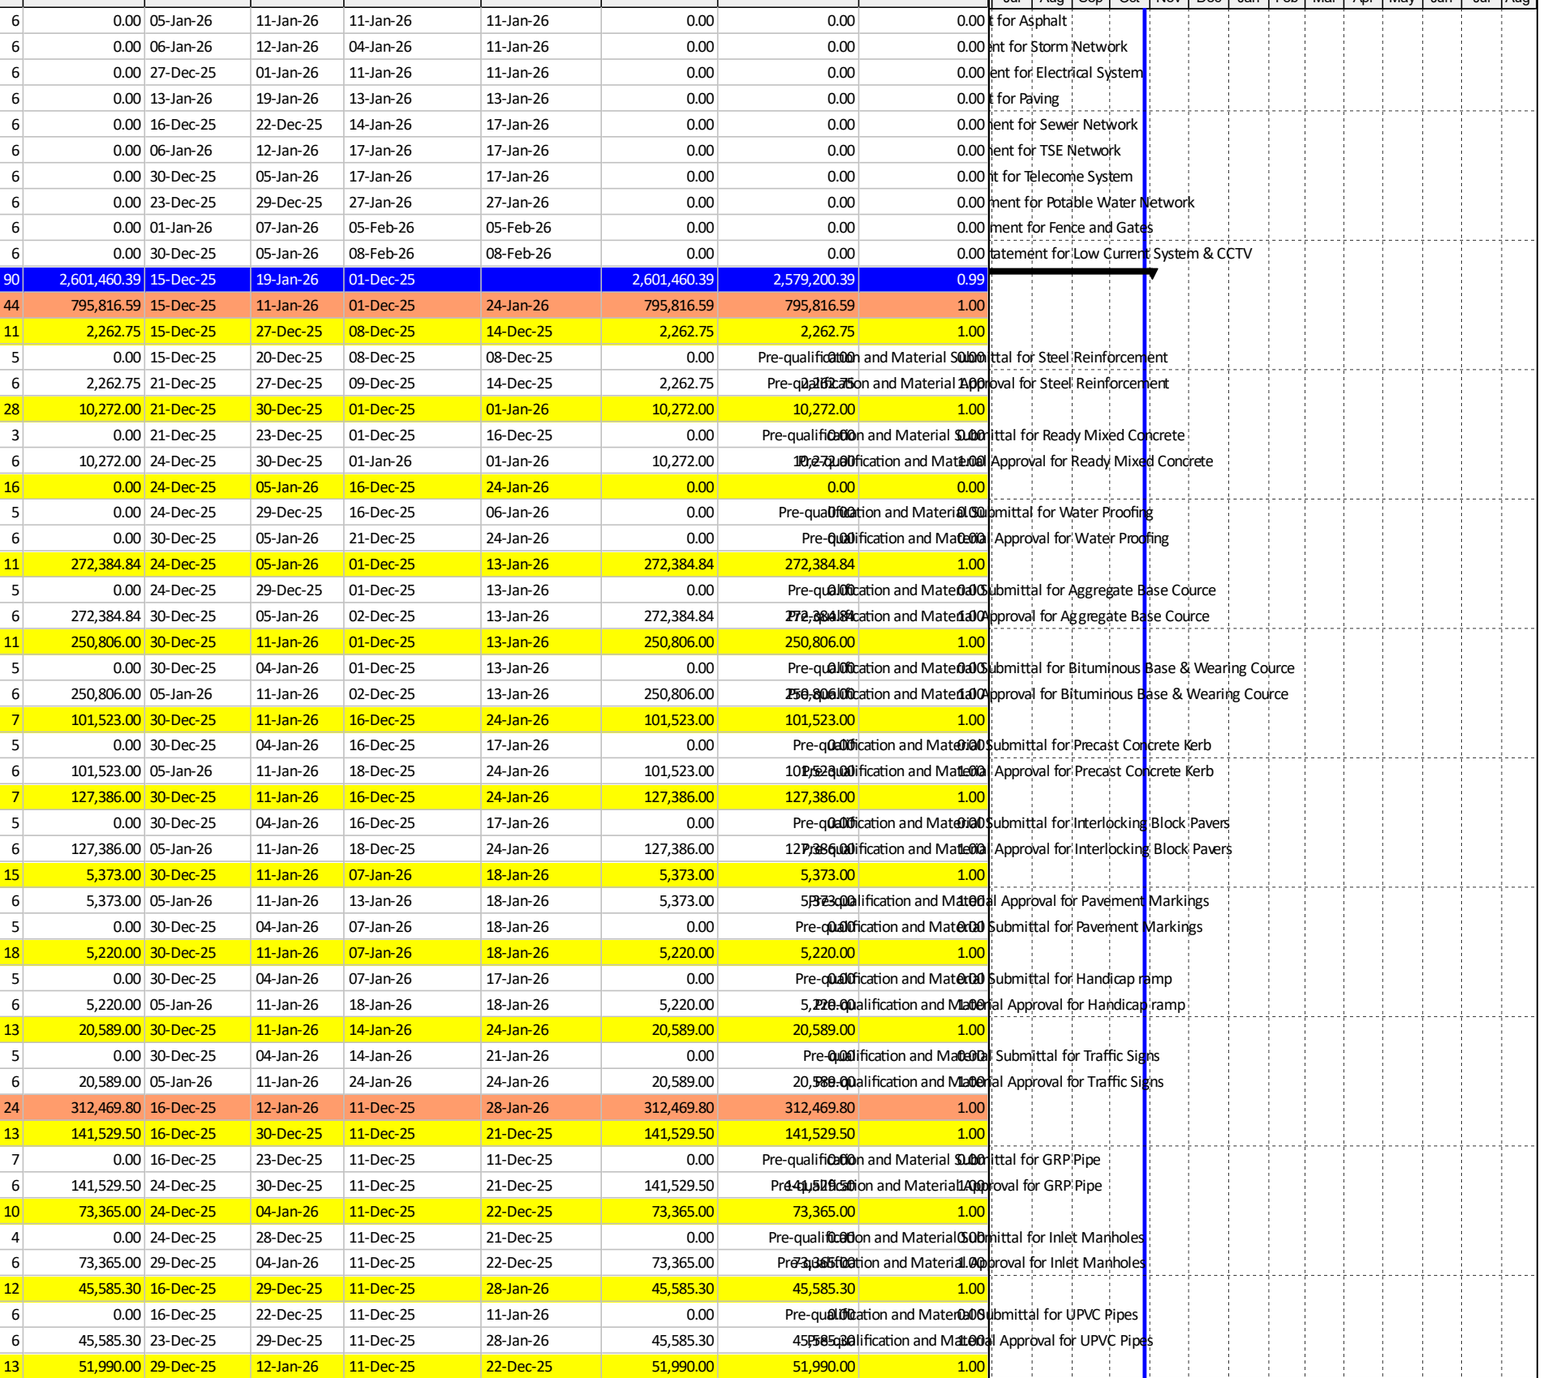


© Oracle Corporation

Activity ID	Activity Name	Original Duration	Budgeted Total Cost	BL Project Start	BL Project Finish	Actual Start	Actual Finish	Planned Value Cost	Earned Value Cost	Schedule Performance Index
CON-LEG101-SB-1620	Pre-qualification and Material Submittal for Concrete chambers	7	0.00	29-Dec-25	05-Jan-26	11-Dec-25	21-Dec-25	0.00	0.00	1.00
CON-LEG101-SB-1630	Pre-qualification and Material Approval for Concrete chambers	6	51,990.00	06-Jan-26	12-Jan-26	11-Dec-25	22-Dec-25	51,990.00	51,990.00	1.00
Sanitary Sewerage		20	170,565.00	16-Dec-25	07-Jan-26	11-Dec-25	28-Dec-25	170,565.00	170,565.00	1.00
GRP Pipes		13	105,885.00	16-Dec-25	30-Dec-25	11-Dec-25	21-Dec-25	105,885.00	105,885.00	1.00
CON-LEG101-SB-1460	Pre-qualification and Material Submittal for GRP Pipe	7	0.00	16-Dec-25	23-Dec-25	11-Dec-25	13-Dec-25	0.00	0.00	1.00
CON-LEG101-SB-1470	Pre-qualification and Material Approval for GRP Pipe	6	105,885.00	24-Dec-25	30-Dec-25	11-Dec-25	21-Dec-25	105,885.00	105,885.00	1.00
Fiberglass Manholes		13	64,680.00	24-Dec-25	07-Jan-26	11-Dec-25	28-Dec-25	64,680.00	64,680.00	1.00
CON-LEG101-SB-1500	Pre-qualification and Material Submittal for Fiberglass Manholes	7	0.00	24-Dec-25	31-Dec-25	11-Dec-25	27-Dec-25	0.00	0.00	1.00
CON-LEG101-SB-1510	Pre-qualification and Material Approval for Fiberglass Manholes	6	64,680.00	01-Jan-26	07-Jan-26	11-Dec-25	28-Dec-25	64,680.00	64,680.00	1.00
TSE Network		18	174,382.50	24-Dec-25	12-Jan-26	13-Dec-25	01-Jan-26	174,382.50	174,382.50	1.00
HDPE Pipe (PN 16)		11	94,747.50	24-Dec-25	05-Jan-26	13-Dec-25	22-Dec-25	94,747.50	94,747.50	1.00
CON-LEG101-SB-1430	Pre-qualification and Material Approval for HDPE Pipe (PN 16)	6	94,747.50	30-Dec-25	05-Jan-26	14-Dec-25	22-Dec-25	94,747.50	94,747.50	1.00
CON-LEG101-SB-1420	Pre-qualification and Material Submittal for HDPE Pipe (PN 16)	5	0.00	24-Dec-25	29-Dec-25	13-Dec-25	22-Dec-25	0.00	0.00	1.00
Fire Hydrant		13	24,030.00	30-Dec-25	11-Jan-26	15-Dec-25	01-Jan-26	24,030.00	24,030.00	1.00
CON-LEG101-SB-2100	Pre-qualification and Material Submittal for Fire Hydrant	5	0.00	30-Dec-25	04-Jan-26	15-Dec-25	29-Dec-25	0.00	0.00	1.00
CON-LEG101-SB-2110	Pre-qualification and Material Approval for Fire Hydrant	6	24,030.00	05-Jan-26	11-Jan-26	17-Dec-25	01-Jan-26	24,030.00	24,030.00	1.00
Valves		10	55,605.00	01-Jan-26	12-Jan-26	15-Dec-25	01-Jan-26	55,605.00	55,605.00	1.00
CON-LEG101-SB-2060	Pre-qualification and Material Submittal for Valves	4	0.00	01-Jan-26	05-Jan-26	15-Dec-25	29-Dec-25	0.00	0.00	1.00
CON-LEG101-SB-2070	Pre-qualification and Material Approval for Valves	6	55,605.00	06-Jan-26	12-Jan-26	17-Dec-25	01-Jan-26	55,605.00	55,605.00	1.00
Public Water Utility Distribution		16	148,263.60	25-Dec-25	11-Jan-26	13-Dec-25	01-Jan-26	148,263.60	148,263.60	1.00
HDPE Pipe (PN 16)		11	110,643.60	25-Dec-25	06-Jan-26	13-Dec-25	22-Dec-25	110,643.60	110,643.60	1.00
CON-LEG101-SB-1380	Pre-qualification and Material Submittal for HDPE Pipe (PN 16)	5	0.00	25-Dec-25	30-Dec-25	13-Dec-25	22-Dec-25	0.00	0.00	1.00
CON-LEG101-SB-1390	Pre-qualification and Material Approval for HDPE Pipe (PN 16)	6	110,643.60	31-Dec-25	06-Jan-26	14-Dec-25	22-Dec-25	110,643.60	110,643.60	1.00
Valves		11	37,620.00	31-Dec-25	11-Jan-26	15-Dec-25	01-Jan-26	37,620.00	37,620.00	1.00
CON-LEG101-SB-2020	Pre-qualification and Material Submittal for Valves	4	0.00	31-Dec-25	04-Jan-26	15-Dec-25	29-Dec-25	0.00	0.00	1.00
CON-LEG101-SB-2030	Pre-qualification and Material Approval for Valves	6	37,620.00	05-Jan-26	11-Jan-26	17-Dec-25	01-Jan-26	37,620.00	37,620.00	1.00
Bridge Works		58	103,509.20	24-Dec-25	11-Jan-26	30-Dec-25	24-Mar-26	103,509.20	103,509.20	1.00
Prestressing Strands		16	71,205.00	24-Dec-25	05-Jan-26	06-Jan-26	31-Jan-26	71,205.00	71,205.00	1.00
CON-LEG101-SB-3740	Pre-qualification and Material Submittal for Prestressing Strands	5	0.00	24-Dec-25	29-Dec-25	06-Jan-26	12-Jan-26	0.00	0.00	1.00
CON-LEG101-SB-3750	Pre-qualification and Material Approval for Prestressing Strands	6	71,205.00	30-Dec-25	05-Jan-26	20-Jan-26	31-Jan-26	71,205.00	71,205.00	1.00
Bridge Bearings		11	1,800.00	30-Dec-25	11-Jan-26	06-Jan-26	31-Jan-26	1,800.00	1,800.00	1.00
CON-LEG101-SB-3780	Pre-qualification and Material Submittal for Bridge Bearings	5	0.00	30-Dec-25	04-Jan-26	06-Jan-26	12-Jan-26	0.00	0.00	1.00
CON-LEG101-SB-3790	Pre-qualification and Material Approval for Bridge Bearings	6	1,800.00	05-Jan-26	11-Jan-26	12-Jan-26	31-Jan-26	1,800.00	1,800.00	1.00
Expansion Joints		19	7,944.20	30-Dec-25	11-Jan-26	07-Jan-26	04-Feb-26	7,944.20	7,944.20	1.00
CON-LEG101-SB-3800	Pre-qualification and Material Submittal for Expansion Joints	5	0.00	30-Dec-25	04-Jan-26	07-Jan-26	17-Jan-26	0.00	0.00	1.00
CON-LEG101-SB-3810	Pre-qualification and Material Approval for Expansion Joints	6	7,944.20	05-Jan-26	11-Jan-26	22-Jan-26	04-Feb-26	7,944.20	7,944.20	1.00
New Jersey		11	1,440.00	30-Dec-25	11-Jan-26	30-Dec-25	01-Jan-26	1,440.00	1,440.00	1.00
CON-LEG101-SB-3760	Pre-qualification and Material Submittal for New Jersey	5	0.00	30-Dec-25	04-Jan-26	30-Dec-25	30-Dec-25	0.00	0.00	1.00
CON-LEG101-SB-3770	Pre-qualification and Material Approval for New Jersey	6	1,440.00	05-Jan-26	11-Jan-26	01-Jan-26	01-Jan-26	1,440.00	1,440.00	1.00
Guard Rail		15	4,320.00	30-Dec-25	11-Jan-26	14-Jan-26	24-Mar-26	4,320.00	4,320.00	1.00
CON-LEG101-SB-3820	Pre-qualification and Material Submittal for Guard Rail	5	0.00	30-Dec-25	04-Jan-26	14-Jan-26	22-Jan-26	0.00	0.00	1.00
CON-LEG101-SB-3830	Pre-qualification and Material Approval for Guard Rail	6	4,320.00	05-Jan-26	11-Jan-26	14-Jan-26	24-Mar-26	4,320.00	4,320.00	1.00
GRP Panel		53	11,280.00	30-Dec-25	11-Jan-26	15-Jan-26	08-Mar-26	11,280.00	11,280.00	1.00
CON-LEG101-SB-3840	Pre-qualification and Material Submittal for GRP Panel	5	0.00	30-Dec-25	04-Jan-26	15-Jan-26	20-Jan-26	0.00	0.00	1.00
CON-LEG101-SB-3850	Pre-qualification and Material Approval for GRP Panel	6	11,280.00	05-Jan-26	11-Jan-26	08-Mar-26	08-Mar-26	11,280.00	11,280.00	1.00
Logo MODON		26	4,800.00	30-Dec-25	11-Jan-26	14-Jan-26	07-Feb-26	4,800.00	4,800.00	1.00
CON-LEG101-SB-3860	Pre-qualification and Material Submittal for Logo MODON	5	0.00	30-Dec-25	04-Jan-26	14-Jan-26	20-Jan-26	0.00	0.00	1.00
CON-LEG101-SB-3870	Pre-qualification and Material Approval for Logo MODON	6	4,800.00	05-Jan-26	11-Jan-26	07-Feb-26	07-Feb-26	4,800.00	4,800.00	1.00
Bridge Gully (Scupper) drainage		30	720.00	30-Dec-25	11-Jan-26	01-Jan-26	05-Feb-26	720.00	720.00	1.00
CON-LEG101-SB-3880	Pre-qualification and Material Submittal for Bridge Gully (Scupper) drai	5	0.00	30-Dec-25	04-Jan-26	01-Jan-26	01-Feb-26	0.00	0.00	1.00
CON-LEG101-SB-3890	Pre-qualification and Material Approval for Bridge Gully (Scupper) drain	6	720.00	05-Jan-26	11-Jan-26	05-Feb-26	05-Feb-26	720.00	720.00	1.00
Fence & Gates		32	353,817.10	20-Dec-25	10-Jan-26	10-Dec-25	24-Jan-26	353,817.10	353,817.10	1.00
Metal Fence		21	341,825.50	20-Dec-25	31-Dec-25	10-Dec-25	06-Jan-26	341,825.50	341,825.50	1.00

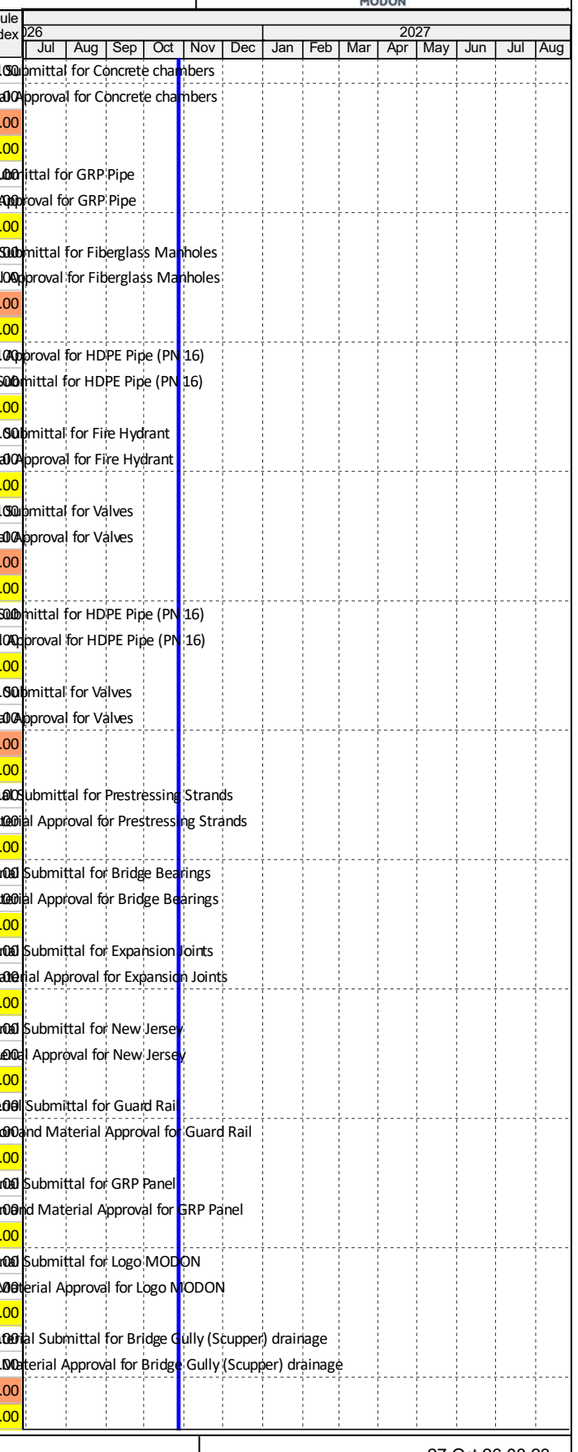


© Oracle Corporation

Activity ID	Activity Name	Original Duration	Budgeted Total Cost	BL Project Start	BL Project Finish	Actual Start	Actual Finish	Planned Value Cost	Earned Value Cost	Schedule Performance Index
CON-LEG101-SB-2270	Pre-qualification and Material Submittal for Metal Fence	5	0.00	20-Dec-25	24-Dec-25	10-Dec-25	05-Jan-26	0.00	0.00	1.00
CON-LEG101-SB-2310	Pre-qualification and Material Approval for Metal Fence	6	341,825.50	25-Dec-25	31-Dec-25	01-Jan-26	06-Jan-26	341,825.50	341,825.50	1.00
Gates		23	4,680.00	23-Dec-25	04-Jan-26	10-Dec-25	06-Jan-26	4,680.00	4,680.00	1.00
CON-LEG101-SB-2290	Pre-qualification and Material Submittal for Gates	5	0.00	23-Dec-25	28-Dec-25	10-Dec-25	05-Jan-26	0.00	0.00	1.00
CON-LEG101-SB-2330	Pre-qualification and Material Approval for Gates	6	4,680.00	29-Dec-25	04-Jan-26	01-Jan-26	06-Jan-26	4,680.00	4,680.00	1.00
Paint On Cement Plaster		24	7,311.60	29-Dec-25	10-Jan-26	16-Dec-25	24-Jan-26	7,311.60	7,311.60	1.00
CON-LEG101-SB-3900	Pre-qualification and Material Submittal for Paint On Cement Plaster	5	0.00	29-Dec-25	03-Jan-26	16-Dec-25	16-Dec-25	0.00	0.00	1.00
CON-LEG101-SB-3910	Pre-qualification and Material Approval for Paint On Cement Plaster	6	7,311.60	04-Jan-26	10-Jan-26	06-Jan-26	24-Jan-26	7,311.60	7,311.60	1.00
Telecommunications		46	102,354.30	20-Dec-25	19-Jan-26	13-Dec-25	24-Jan-26	102,354.30	102,354.30	1.00
Pipe for the Duct		13	63,084.30	20-Dec-25	03-Jan-26	13-Dec-25	21-Jan-26	63,084.30	63,084.30	1.00
CON-LEG101-SB-3340	Pre-qualification and Material Submittal for Pipe for the Duct	7	0.00	20-Dec-25	27-Dec-25	13-Dec-25	18-Jan-26	0.00	0.00	1.00
CON-LEG101-SB-3350	Pre-qualification and Material Approval for Pipe for the Duct	6	63,084.30	28-Dec-25	03-Jan-26	14-Dec-25	21-Jan-26	63,084.30	63,084.30	1.00
Low Voltage Cables		19	0.00	28-Dec-25	10-Jan-26	30-Dec-25	24-Jan-26	0.00	0.00	0.00
CON-LEG101-SB-3380	Pre-qualification and Material Submittal for Low Voltage Cables	6	0.00	28-Dec-25	03-Jan-26	30-Dec-25	14-Jan-26	0.00	0.00	1.00
CON-LEG101-SB-3390	Pre-qualification and Material Approval for Low Voltage Cables	6	0.00	04-Jan-26	10-Jan-26	04-Jan-26	24-Jan-26	0.00	0.00	0.00
Manhole		14	39,270.00	04-Jan-26	19-Jan-26	01-Jan-26	06-Jan-26	39,270.00	39,270.00	1.00
CON-LEG101-SB-3360	Pre-qualification and Material Submittal for Manhole	8	0.00	04-Jan-26	12-Jan-26	01-Jan-26	01-Jan-26	0.00	0.00	1.00
CON-LEG101-SB-3370	Pre-qualification and Material Approval for Manhole	6	39,270.00	13-Jan-26	19-Jan-26	06-Jan-26	06-Jan-26	39,270.00	39,270.00	1.00
Electrical Network		52	274,089.80	20-Dec-25	12-Jan-26	13-Dec-25		274,089.80	251,829.80	0.92
Pipe for the Duct		13	16,054.80	20-Dec-25	03-Jan-26	13-Dec-25	21-Jan-26	16,054.80	16,054.80	1.00
CON-LEG101-SB-1240	Pre-qualification and Material Submittal for Pipe for the Duct	7	0.00	20-Dec-25	27-Dec-25	13-Dec-25	18-Jan-26	0.00	0.00	1.00
CON-LEG101-SB-1270	Pre-qualification and Material Approval for Pipe for the Duct	6	16,054.80	28-Dec-25	03-Jan-26	14-Dec-25	21-Jan-26	16,054.80	16,054.80	1.00
Low Voltage Cables		16	46,446.00	28-Dec-25	06-Jan-26	30-Dec-25	24-Jan-26	46,446.00	46,446.00	1.00
CON-LEG101-SB-1780	Pre-qualification and Material Submittal for Low Voltage Cables	3	0.00	28-Dec-25	30-Dec-25	30-Dec-25	14-Jan-26	0.00	0.00	1.00
CON-LEG101-SB-1790	Pre-qualification and Material Approval for Low Voltage Cables	6	46,446.00	31-Dec-25	06-Jan-26	04-Jan-26	24-Jan-26	46,446.00	46,446.00	1.00
Lighting poles		20	45,186.00	31-Dec-25	12-Jan-26	28-Dec-25	24-Jan-26	45,186.00	45,186.00	1.00
CON-LEG101-SB-1820	Pre-qualification and Material Submittal for Lighting poles	5	0.00	31-Dec-25	05-Jan-26	28-Dec-25	14-Jan-26	0.00	0.00	1.00
CON-LEG101-SB-1830	Pre-qualification and Material Approval for Lighting poles	6	45,186.00	06-Jan-26	12-Jan-26	04-Jan-26	24-Jan-26	45,186.00	45,186.00	1.00
Street Lighting Luminaire		20	13,290.00	31-Dec-25	12-Jan-26	28-Dec-25	24-Jan-26	13,290.00	13,290.00	1.00
CON-LEG101-SB-1860	Pre-qualification and Material Submittal for Street Lighting Luminaire	5	0.00	31-Dec-25	05-Jan-26	28-Dec-25	14-Jan-26	0.00	0.00	1.00
CON-LEG101-SB-1870	Pre-qualification and Material Approval for Street Lighting Luminaire	6	13,290.00	06-Jan-26	12-Jan-26	06-Jan-26	24-Jan-26	13,290.00	13,290.00	1.00
Medium Voltage Cable		17	96,000.00	31-Dec-25	12-Jan-26	30-Dec-25	05-Feb-26	96,000.00	96,000.00	1.00
CON-LEG101-SB-1660	Pre-qualification and Material Submittal for Medium Voltage Cable	5	0.00	31-Dec-25	05-Jan-26	30-Dec-25	28-Jan-26	0.00	0.00	1.00
CON-LEG101-SB-1670	Pre-qualification and Material Approval for Medium Voltage Cable	6	96,000.00	06-Jan-26	12-Jan-26	04-Jan-26	05-Feb-26	96,000.00	96,000.00	1.00
Cable Termination & Joints		9	5,828.00	31-Dec-25	10-Jan-26	30-Dec-25	05-Feb-26	5,828.00	5,828.00	1.00
CON-LEG101-SB-1300	Pre-qualification and Material Submittal for Cable Termination & Joints	3	0.00	31-Dec-25	03-Jan-26	30-Dec-25	28-Jan-26	0.00	0.00	1.00
CON-LEG101-SB-1310	Pre-qualification and Material Approval for Cable Termination & Joints	6	5,828.00	04-Jan-26	10-Jan-26	04-Jan-26	05-Feb-26	5,828.00	5,828.00	1.00
Ring Main Unit		22	21,600.00	31-Dec-25	10-Jan-26	13-Jan-26		21,600.00	6,480.00	0.30
CON-LEG101-SB-1700	Pre-qualification and Material Submittal for Ring Main Unit	3	0.00	31-Dec-25	03-Jan-26	14-Jan-26	14-Jan-26	0.00	0.00	1.00
CON-LEG101-SB-1710	Pre-qualification and Material Approval for Ring Main Unit	6	21,600.00	04-Jan-26	10-Jan-26	13-Jan-26		21,600.00	6,480.00	0.30
Street Lighting Sub-station		22	10,200.00	31-Dec-25	10-Jan-26	13-Jan-26		10,200.00	3,060.00	0.30
CON-LEG101-SB-1740	Pre-qualification and Material Submittal for Street Lighting Sub-station	3	0.00	31-Dec-25	03-Jan-26	14-Jan-26	14-Jan-26	0.00	0.00	1.00
CON-LEG101-SB-1750	Pre-qualification and Material Approval for Street Lighting Sub-station	6	10,200.00	04-Jan-26	10-Jan-26	13-Jan-26		10,200.00	3,060.00	0.30
Earthing System		6	5,385.00	31-Dec-25	10-Jan-26	14-Jan-26	21-Jan-26	5,385.00	5,385.00	1.00
CON-LEG101-SB-1340	Pre-qualification and Material Submittal for Earthing System	3	0.00	31-Dec-25	03-Jan-26	14-Jan-26	14-Jan-26	0.00	0.00	1.00
CON-LEG101-SB-1350	Pre-qualification and Material Approval for Earthing System	6	5,385.00	04-Jan-26	10-Jan-26	21-Jan-26	21-Jan-26	5,385.00	5,385.00	1.00
Lighting panels		22	2,400.00	31-Dec-25	10-Jan-26	13-Jan-26	15-Apr-26	2,400.00	2,400.00	1.00
CON-LEG101-SB-2390	Pre-qualification and Material Submittal for Lighting panels	3	0.00	31-Dec-25	03-Jan-26	14-Jan-26	14-Jan-26	0.00	0.00	1.00
CON-LEG101-SB-2430	Pre-qualification and Material Approval for Lighting panels	6	2,400.00	04-Jan-26	10-Jan-26	13-Jan-26	15-Apr-26	2,400.00	2,400.00	1.00
System for KWHM		22	1,200.00	31-Dec-25	10-Jan-26	13-Jan-26	15-Apr-26	1,200.00	1,200.00	1.00
CON-LEG101-SB-1900	Pre-qualification and Material Submittal for System for KWHM	3	0.00	31-Dec-25	03-Jan-26	14-Jan-26	14-Jan-26	0.00	0.00	1.00
CON-LEG101-SB-1910	Pre-qualification and Material Approval for System for KWHM	6	1,200.00	04-Jan-26	10-Jan-26	13-Jan-26	15-Apr-26	1,200.00	1,200.00	1.00
Feeder Piller		22	10,500.00	31-Dec-25	10-Jan-26	13-Jan-26	15-Apr-26	10,500.00	10,500.00	1.00

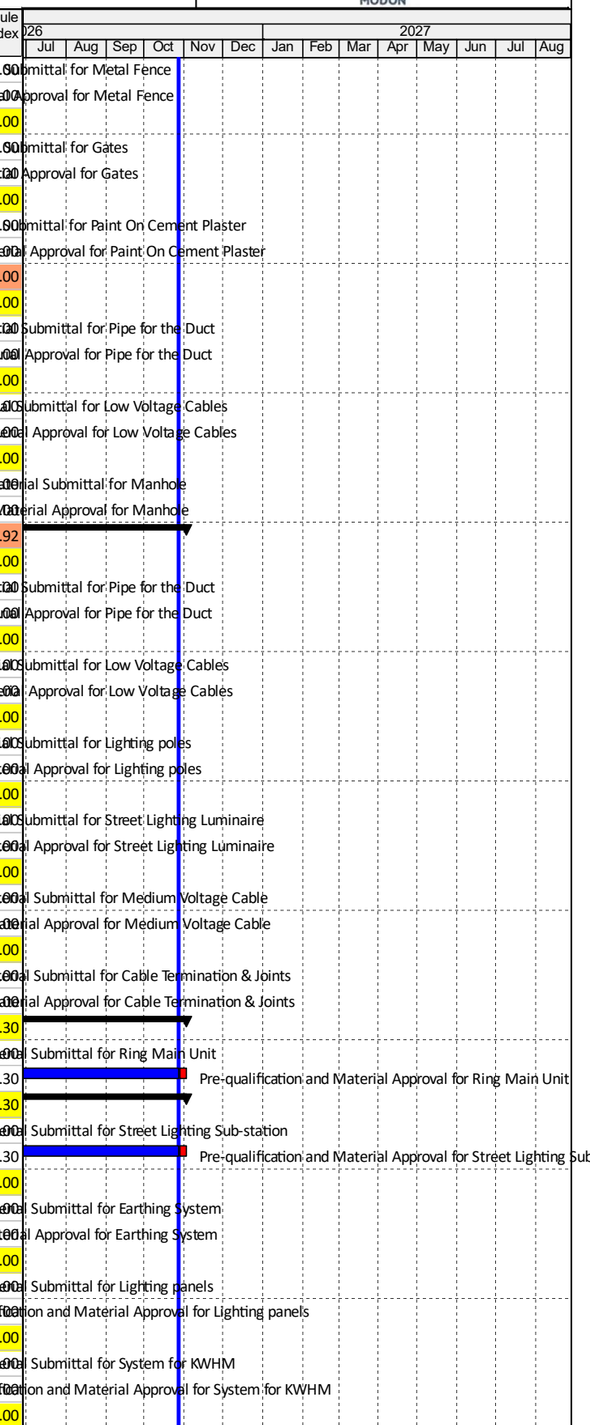


© Oracle Corporation

Activity ID	Activity Name	Original Duration	Budgeted Total Cost	BL Project Start	BL Project Finish	Actual Start	Actual Finish	Planned Value Cost	Earned Value Cost	Schedule Performance Index
CON-LEG101-SB-1940	Pre-qualification and Material Submittal for Feeder Piller	3	0.00	31-Dec-25	03-Jan-26	14-Jan-26	14-Jan-26	0.00	0.00	0.00
CON-LEG101-SB-1950	Pre-qualification and Material Approval for Feeder Piller	6	10,500.00	04-Jan-26	10-Jan-26	13-Jan-26	15-Apr-26	10,500.00	10,500.00	1.00
Street Lighting Panels		22	0.00	31-Dec-25	10-Jan-26	14-Jan-26	15-Apr-26	0.00	0.00	0.00
CON-LEG101-SB-1980	Pre-qualification and Material Submittal for Street Lighting Panels	3	0.00	31-Dec-25	03-Jan-26	14-Jan-26	14-Jan-26	0.00	0.00	0.00
CON-LEG101-SB-1990	Pre-qualification and Material Approval for Street Lighting Panels	6	0.00	04-Jan-26	10-Jan-26	14-Jan-26	15-Apr-26	0.00	0.00	0.00
CCTV feeding system and GSM		14	74,520.00	28-Dec-25	19-Jan-26	12-Jan-26	05-Apr-26	74,520.00	74,520.00	1.00
Fiber Optic Patch Panel 12 port		8	10,740.00	28-Dec-25	10-Jan-26	12-Jan-26	05-Apr-26	10,740.00	10,740.00	1.00
CON-LEG101-SB-3400	Pre-qualification and Material Submittal for Fiber Optic Patch Panel 12	6	0.00	28-Dec-25	03-Jan-26	12-Jan-26	15-Jan-26	0.00	0.00	0.00
CON-LEG101-SB-3410	Pre-qualification and Material Approval for Fiber Optic Patch Panel 12 p	6	10,740.00	04-Jan-26	10-Jan-26	20-Jan-26	05-Apr-26	10,740.00	10,740.00	1.00
Modular Industrial Switches for main pole		7	450.00	04-Jan-26	13-Jan-26	12-Jan-26	05-Apr-26	450.00	450.00	1.00
CON-LEG101-SB-3500	Pre-qualification and Material Submittal for Modular Industrial Switche	3	0.00	04-Jan-26	06-Jan-26	12-Jan-26	15-Jan-26	0.00	0.00	0.00
CON-LEG101-SB-3510	Pre-qualification and Material Approval for Modular Industrial Switches	6	450.00	07-Jan-26	13-Jan-26	20-Jan-26	05-Apr-26	450.00	450.00	1.00
8POE ports Industrial Switches for remote poles		12	1,800.00	07-Jan-26	19-Jan-26	12-Jan-26	05-Apr-26	1,800.00	1,800.00	1.00
CON-LEG101-SB-3440	Pre-qualification and Material Submittal for 8POE ports Industrial Swit	5	0.00	07-Jan-26	12-Jan-26	12-Jan-26	15-Jan-26	0.00	0.00	0.00
CON-LEG101-SB-3450	Pre-qualification and Material Approval for 8POE ports Industrial Switcl	6	1,800.00	13-Jan-26	19-Jan-26	20-Jan-26	05-Apr-26	1,800.00	1,800.00	1.00
Core Switch		12	1,800.00	07-Jan-26	19-Jan-26	12-Jan-26	05-Apr-26	1,800.00	1,800.00	1.00
CON-LEG101-SB-3420	Pre-qualification and Material Submittal for Core Switch	5	0.00	07-Jan-26	12-Jan-26	12-Jan-26	15-Jan-26	0.00	0.00	0.00
CON-LEG101-SB-3430	Pre-qualification and Material Approval for Core Switch	6	1,800.00	13-Jan-26	19-Jan-26	20-Jan-26	05-Apr-26	1,800.00	1,800.00	1.00
Access Switch 48 port		12	900.00	07-Jan-26	19-Jan-26	12-Jan-26	05-Apr-26	900.00	900.00	1.00
CON-LEG101-SB-3460	Pre-qualification and Material Submittal for Access Switch 48 port	5	0.00	07-Jan-26	12-Jan-26	12-Jan-26	15-Jan-26	0.00	0.00	0.00
CON-LEG101-SB-3470	Pre-qualification and Material Approval for Access Switch 48 port	6	900.00	13-Jan-26	19-Jan-26	20-Jan-26	05-Apr-26	900.00	900.00	1.00
Server		12	5,850.00	07-Jan-26	19-Jan-26	12-Jan-26	05-Apr-26	5,850.00	5,850.00	1.00
CON-LEG101-SB-3480	Pre-qualification and Material Submittal for Server	5	0.00	07-Jan-26	12-Jan-26	12-Jan-26	15-Jan-26	0.00	0.00	0.00
CON-LEG101-SB-3490	Pre-qualification and Material Approval for Server	6	5,850.00	13-Jan-26	19-Jan-26	20-Jan-26	05-Apr-26	5,850.00	5,850.00	1.00
Stand rack 42U- 19"		12	900.00	07-Jan-26	19-Jan-26	12-Jan-26	05-Apr-26	900.00	900.00	1.00
CON-LEG101-SB-3520	Pre-qualification and Material Submittal for Stand rack 42U- 19"	5	0.00	07-Jan-26	12-Jan-26	12-Jan-26	15-Jan-26	0.00	0.00	0.00
CON-LEG101-SB-3530	Pre-qualification and Material Approval for Stand rack 42U- 19"	6	900.00	13-Jan-26	19-Jan-26	20-Jan-26	05-Apr-26	900.00	900.00	1.00
IP Outdoor CCTV POE Camera,5 MP, Metal Housing		12	4,200.00	07-Jan-26	19-Jan-26	12-Jan-26	05-Apr-26	4,200.00	4,200.00	1.00
CON-LEG101-SB-3620	Pre-qualification and Material Submittal for IP Outdoor CCTV POE Cam	5	0.00	07-Jan-26	12-Jan-26	12-Jan-26	15-Jan-26	0.00	0.00	0.00
CON-LEG101-SB-3630	Pre-qualification and Material Approval for IP Outdoor CCTV POE Came	6	4,200.00	13-Jan-26	19-Jan-26	20-Jan-26	05-Apr-26	4,200.00	4,200.00	1.00
Outdoor PTZ with IR, HDTV 1080 and 31x optical, 12x digital		12	7,350.00	07-Jan-26	19-Jan-26	12-Jan-26	05-Apr-26	7,350.00	7,350.00	1.00
CON-LEG101-SB-3540	Pre-qualification and Material Submittal for Outdoor PTZ with IR, HDTV	5	0.00	07-Jan-26	12-Jan-26	12-Jan-26	15-Jan-26	0.00	0.00	0.00
CON-LEG101-SB-3550	Pre-qualification and Material Approval for Outdoor PTZ with IR, HDTV	6	7,350.00	13-Jan-26	19-Jan-26	20-Jan-26	05-Apr-26	7,350.00	7,350.00	1.00
Security workstation with 1 x 19" LED screen		12	750.00	07-Jan-26	19-Jan-26	12-Jan-26	05-Apr-26	750.00	750.00	1.00
CON-LEG101-SB-3560	Pre-qualification and Material Submittal for Security workstation with 1	5	0.00	07-Jan-26	12-Jan-26	12-Jan-26	15-Jan-26	0.00	0.00	0.00
CON-LEG101-SB-3570	Pre-qualification and Material Approval for Security workstation with 1	6	750.00	13-Jan-26	19-Jan-26	20-Jan-26	05-Apr-26	750.00	750.00	1.00
LED Screen 43" (24/7 operation) with Ethernet decoders		12	1,800.00	07-Jan-26	19-Jan-26	12-Jan-26	05-Apr-26	1,800.00	1,800.00	1.00
CON-LEG101-SB-3580	Pre-qualification and Material Submittal for LED Screen 43" (24/7 opera	5	0.00	07-Jan-26	12-Jan-26	12-Jan-26	15-Jan-26	0.00	0.00	0.00
CON-LEG101-SB-3590	Pre-qualification and Material Approval for LED Screen 43" (24/7 operat	6	1,800.00	13-Jan-26	19-Jan-26	20-Jan-26	05-Apr-26	1,800.00	1,800.00	1.00
Network Video Recorder 4k 64 Channel		12	1,500.00	07-Jan-26	19-Jan-26	12-Jan-26	05-Apr-26	1,500.00	1,500.00	1.00
CON-LEG101-SB-3600	Pre-qualification and Material Submittal for Network Video Recorder 4k	5	0.00	07-Jan-26	12-Jan-26	12-Jan-26	15-Jan-26	0.00	0.00	0.00
CON-LEG101-SB-3610	Pre-qualification and Material Approval for Network Video Recorder 4k	6	1,500.00	13-Jan-26	19-Jan-26	20-Jan-26	05-Apr-26	1,500.00	1,500.00	1.00
Keypad		12	3,000.00	07-Jan-26	19-Jan-26	12-Jan-26	05-Apr-26	3,000.00	3,000.00	1.00
CON-LEG101-SB-3640	Pre-qualification and Material Submittal for Keypad	5	0.00	07-Jan-26	12-Jan-26	12-Jan-26	15-Jan-26	0.00	0.00	0.00
CON-LEG101-SB-3650	Pre-qualification and Material Approval for Keypad	6	3,000.00	13-Jan-26	19-Jan-26	20-Jan-26	05-Apr-26	3,000.00	3,000.00	1.00
Horizontal Power Distribution Unit (min 8 outlets)		12	600.00	07-Jan-26	19-Jan-26	12-Jan-26	05-Apr-26	600.00	600.00	1.00
CON-LEG101-SB-3660	Pre-qualification and Material Submittal for Horizontal Power Distributi	5	0.00	07-Jan-26	12-Jan-26	12-Jan-26	15-Jan-26	0.00	0.00	0.00
CON-LEG101-SB-3670	Pre-qualification and Material Approval for Horizontal Power Distributio	6	600.00	13-Jan-26	19-Jan-26	20-Jan-26	05-Apr-26	600.00	600.00	1.00
35 Meters mono pole with Double Platform for Access Points		7	4,800.00	07-Jan-26	19-Jan-26	12-Jan-26	05-Apr-26	4,800.00	4,800.00	1.00
CON-LEG101-SB-3680	Pre-qualification and Material Submittal for 35 Meters mono pole with	5	0.00	07-Jan-26	12-Jan-26	12-Jan-26	15-Jan-26	0.00	0.00	0.00
CON-LEG101-SB-3690	Pre-qualification and Material Approval for 35 Meters mono pole with D	6	4,800.00	13-Jan-26	19-Jan-26	20-Jan-26	05-Apr-26	4,800.00	4,800.00	1.00
25 Meters pole for CCTV Cameras		7	23,400.00	07-Jan-26	19-Jan-26	12-Jan-26	05-Apr-26	23,400.00	23,400.00	1.00
CON-LEG101-SB-3700	Pre-qualification and Material Submittal for 25 Meters pole for CCTV C	5	0.00	07-Jan-26	12-Jan-26	12-Jan-26	15-Jan-26	0.00	0.00	0.00

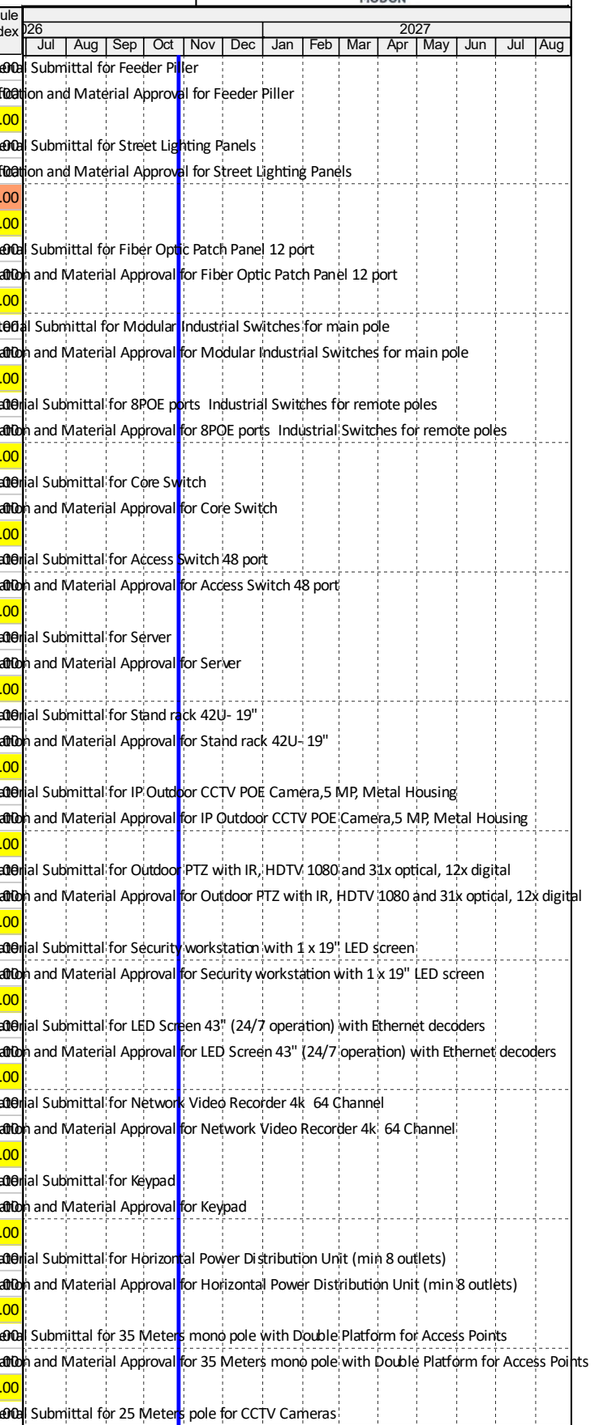


© Oracle Corporation

Activity ID	Activity Name	Original Duration	Budgeted Total Cost	BL Project Start	BL Project Finish	Actual Start	Actual Finish	Planned Value Cost	Earned Value Cost	Schedule Performance Index
CON-LEG101-SB-3710	Pre-qualification and Material Approval for 25 Meters pole for CCTV Ca	6	23,400.00	13-Jan-26	19-Jan-26	20-Jan-26	05-Apr-26	23,400.00	23,400.00	1.00
Short Range wireless point to point wireless bridge		12	4,680.00	07-Jan-26	19-Jan-26	12-Jan-26	05-Apr-26	4,680.00	4,680.00	1.00
CON-LEG101-SB-3720	Pre-qualification and Material Submittal for Short Range wireless point	5	0.00	07-Jan-26	12-Jan-26	12-Jan-26	15-Jan-26	0.00	0.00	0.00
CON-LEG101-SB-3730	Pre-qualification and Material Approval for Short Range wireless point t	6	4,680.00	13-Jan-26	19-Jan-26	20-Jan-26	05-Apr-26	4,680.00	4,680.00	1.00
Irrigation Works		13	56,049.00	30-Dec-25	15-Jan-26	03-Jan-26	19-Feb-26	56,049.00	56,049.00	1.00
16 mm dia (O.D.) linear low density polyethylene tubing		11	32,814.00	30-Dec-25	11-Jan-26	03-Jan-26	06-Jan-26	32,814.00	32,814.00	1.00
CON-LEG101-SB-3930	Pre-qualification and Material Submittal for Steel Fence for 16 mm dia	5	0.00	30-Dec-25	04-Jan-26	03-Jan-26	03-Jan-26	0.00	0.00	0.00
CON-LEG101-SB-3950	Pre-qualification and Material Approval for Steel Fence for 16 mm dia (	6	32,814.00	05-Jan-26	11-Jan-26	06-Jan-26	06-Jan-26	32,814.00	32,814.00	1.00
Irrigation Controller		12	16,305.00	01-Jan-26	13-Jan-26	13-Jan-26	19-Feb-26	16,305.00	16,305.00	1.00
CON-LEG101-SB-3960	Pre-qualification and Material Submittal for Steel Fence for Irrigation C	5	0.00	01-Jan-26	06-Jan-26	13-Jan-26	13-Jan-26	0.00	0.00	0.00
CON-LEG101-SB-3970	Pre-qualification and Material Approval for Steel Fence for Irrigation Co	6	16,305.00	07-Jan-26	13-Jan-26	20-Jan-26	19-Feb-26	16,305.00	16,305.00	1.00
Single station decoder		11	1,200.00	03-Jan-26	14-Jan-26	13-Jan-26	19-Feb-26	1,200.00	1,200.00	1.00
CON-LEG101-SB-3980	Pre-qualification and Material Submittal for Steel Fence for Single stati	5	0.00	03-Jan-26	07-Jan-26	13-Jan-26	13-Jan-26	0.00	0.00	0.00
CON-LEG101-SB-3990	Pre-qualification and Material Approval for Steel Fence for Single statio	6	1,200.00	08-Jan-26	14-Jan-26	20-Jan-26	19-Feb-26	1,200.00	1,200.00	1.00
Decoder cables 12 AWG		10	0.00	04-Jan-26	15-Jan-26	13-Jan-26	19-Feb-26	0.00	0.00	0.00
CON-LEG101-SB-4000	Pre-qualification and Material Submittal for Steel Fence for Decoder ca	5	0.00	04-Jan-26	08-Jan-26	13-Jan-26	13-Jan-26	0.00	0.00	0.00
CON-LEG101-SB-4010	Pre-qualification and Material Approval for Steel Fence for Decoder cab	6	0.00	10-Jan-26	15-Jan-26	26-Jan-26	19-Feb-26	0.00	0.00	0.00
Flush valve		10	5,730.00	04-Jan-26	15-Jan-26	13-Jan-26	19-Feb-26	5,730.00	5,730.00	1.00
CON-LEG101-SB-3920	Pre-qualification and Material Submittal for Steel Gate for Flush valve	5	0.00	04-Jan-26	08-Jan-26	13-Jan-26	13-Jan-26	0.00	0.00	0.00
CON-LEG101-SB-3940	Pre-qualification and Material Approval for Steel Gate for Flush valve	6	5,730.00	10-Jan-26	15-Jan-26	20-Jan-26	19-Feb-26	5,730.00	5,730.00	1.00
Landscape Works		77	35,623.50	30-Dec-25	12-Jan-26	11-Dec-25	02-Mar-26	35,623.50	35,623.50	1.00
HDPE Pipes		9	4,320.00	30-Dec-25	08-Jan-26	11-Dec-25	22-Dec-25	4,320.00	4,320.00	1.00
CON-LEG101-SB-4020	Pre-qualification and Material Submittal for HDPE Pipes	3	0.00	30-Dec-25	01-Jan-26	11-Dec-25	22-Dec-25	0.00	0.00	0.00
CON-LEG101-SB-4040	Pre-qualification and Material Approval for HDPE Pipes	6	4,320.00	03-Jan-26	08-Jan-26	13-Dec-25	22-Dec-25	4,320.00	4,320.00	1.00
Decoder Cables		12	0.00	03-Jan-26	12-Jan-26	13-Jan-26	19-Feb-26	0.00	0.00	0.00
CON-LEG101-SB-4140	Pre-qualification and Material Submittal for Decoder Cables	3	0.00	03-Jan-26	05-Jan-26	13-Jan-26	13-Jan-26	0.00	0.00	0.00
CON-LEG101-SB-4150	Pre-qualification and Material Approval for Decoder Cables	6	0.00	06-Jan-26	12-Jan-26	20-Jan-26	19-Feb-26	0.00	0.00	0.00
Curbs and edging		7	1,224.00	03-Jan-26	12-Jan-26	27-Dec-25	16-Feb-26	1,224.00	1,224.00	1.00
CON-LEG101-SB-4180	Pre-qualification and Material Submittal for Curbs and edging	3	0.00	03-Jan-26	05-Jan-26	27-Dec-25	15-Feb-26	0.00	0.00	0.00
CON-LEG101-SB-4190	Pre-qualification and Material Approval for Curbs and edging	6	1,224.00	06-Jan-26	12-Jan-26	30-Dec-25	16-Feb-26	1,224.00	1,224.00	1.00
Electrical Solenoid Valve		12	0.00	03-Jan-26	12-Jan-26	13-Jan-26	19-Feb-26	0.00	0.00	0.00
CON-LEG101-SB-4030	Pre-qualification and Material Submittal for Electrical Solenoid Valve	3	0.00	03-Jan-26	05-Jan-26	13-Jan-26	13-Jan-26	0.00	0.00	0.00
CON-LEG101-SB-4050	Pre-qualification and Material Approval for Electrical Solenoid Valve	6	0.00	06-Jan-26	12-Jan-26	20-Jan-26	19-Feb-26	0.00	0.00	0.00
Quick coupler valve		12	0.00	03-Jan-26	12-Jan-26	13-Jan-26	19-Feb-26	0.00	0.00	0.00
CON-LEG101-SB-4060	Pre-qualification and Material Submittal for Quick coupler valve	3	0.00	03-Jan-26	05-Jan-26	13-Jan-26	13-Jan-26	0.00	0.00	0.00
CON-LEG101-SB-4070	Pre-qualification and Material Approval for Quick coupler valve	6	0.00	06-Jan-26	12-Jan-26	20-Jan-26	19-Feb-26	0.00	0.00	0.00
Flush valve		12	0.00	03-Jan-26	12-Jan-26	13-Jan-26	19-Feb-26	0.00	0.00	0.00
CON-LEG101-SB-4080	Pre-qualification and Material Submittal for Flush valve	3	0.00	03-Jan-26	05-Jan-26	13-Jan-26	13-Jan-26	0.00	0.00	0.00
CON-LEG101-SB-4090	Pre-qualification and Material Approval for Flush valve	6	0.00	06-Jan-26	12-Jan-26	20-Jan-26	19-Feb-26	0.00	0.00	0.00
Irrigation controller		12	0.00	03-Jan-26	12-Jan-26	13-Jan-26	19-Feb-26	0.00	0.00	0.00
CON-LEG101-SB-4100	Pre-qualification and Material Submittal for Irrigation controller	3	0.00	03-Jan-26	05-Jan-26	13-Jan-26	13-Jan-26	0.00	0.00	0.00
CON-LEG101-SB-4110	Pre-qualification and Material Approval for Irrigation controller	6	0.00	06-Jan-26	12-Jan-26	20-Jan-26	19-Feb-26	0.00	0.00	0.00
Decoder for valve		12	0.00	03-Jan-26	12-Jan-26	13-Jan-26	19-Feb-26	0.00	0.00	0.00
CON-LEG101-SB-4120	Pre-qualification and Material Submittal for Decoder for valve	3	0.00	03-Jan-26	05-Jan-26	13-Jan-26	13-Jan-26	0.00	0.00	0.00
CON-LEG101-SB-4130	Pre-qualification and Material Approval for Decoder for valve	6	0.00	06-Jan-26	12-Jan-26	20-Jan-26	19-Feb-26	0.00	0.00	0.00
Shrubs And Ground Cover		60	30,079.50	03-Jan-26	12-Jan-26	13-Jan-26	02-Mar-26	30,079.50	30,079.50	1.00
CON-LEG101-SB-4160	Pre-qualification and Material Submittal for agricultural soil	3	0.00	03-Jan-26	05-Jan-26	13-Jan-26	13-Jan-26	0.00	0.00	0.00
CON-LEG101-SB-4170	Pre-qualification and Material Approval for agricultural soil	6	30,079.50	06-Jan-26	12-Jan-26	22-Jan-26	02-Mar-26	30,079.50	30,079.50	1.00
Procurement		503	17,355,662.10	28-Dec-25	14-Sep-27	25-Nov-25		13,535,185.10	15,922,584.10	1.18
Short Lead Item		503	6,936,333.10	28-Dec-25	06-Apr-27	25-Nov-25		4,629,253.10	6,708,705.10	1.45
Road Works - Civil		503	6,936,333.10	28-Dec-25	06-Apr-27	25-Nov-25		4,629,253.10	6,708,705.10	1.45
Steel Reinforcement		24	167,565.00	28-Dec-25	24-Jan-26	02-Dec-25	02-Apr-26	167,565.00	167,565.00	1.00
CON-LEG101-PR-1390	PO for Steel Reinforcement	3	0.00	28-Dec-25	30-Dec-25	02-Dec-25	02-Dec-25	0.00	0.00	0.00

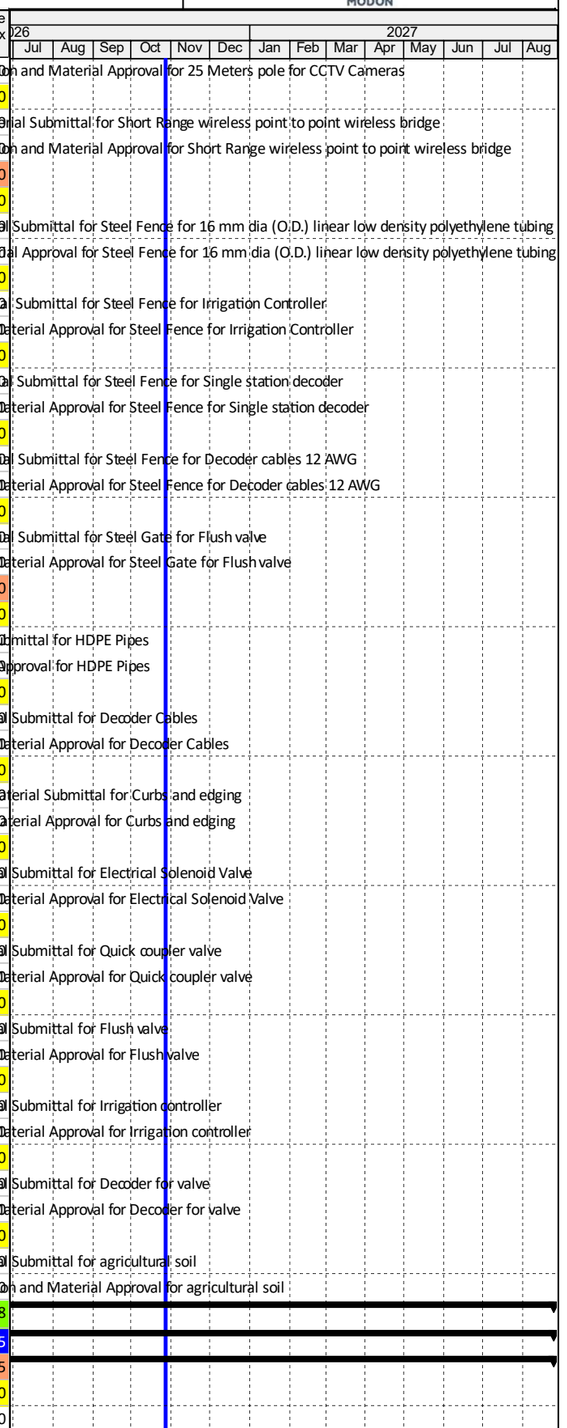


© Oracle Corporation

Activity ID	Activity Name	Original Duration	Budgeted Total Cost	BL Project Start	BL Project Finish	Actual Start	Actual Finish	Planned Value Cost	Earned Value Cost	Schedule Performance Index
CON-LEG101-PR-1410	Material Delivery for Steel Reinforcement	21	167,565.00	31-Dec-25	24-Jan-26	16-Dec-25	02-Apr-26	167,565.00	167,565.00	1.00
Ready Mixed Concrete		29	1,601,570.10	31-Dec-25	17-Feb-26	17-Dec-25	31-Mar-26	1,601,570.10	1,601,570.10	1.00
CON-LEG101-PR-1420	PO for Ready Mixed Concrete	5	0.00	31-Dec-25	05-Jan-26	17-Dec-25	17-Dec-25	0.00	0.00	0.00
CON-LEG101-PR-1430	Material Delivery for Ready Mixed Concrete	21	1,601,570.10	25-Jan-26	17-Feb-26	21-Dec-25	31-Mar-26	1,601,570.10	1,601,570.10	1.00
Backfilling Materials		44	1,529,448.00	06-Jan-26	26-Feb-26	25-Nov-25	31-Mar-26	1,529,448.00	1,529,448.00	1.00
CON-LEG101-PR-3990	PO for Backfilling Materials	5	0.00	06-Jan-26	11-Jan-26	25-Nov-25	25-Nov-25	0.00	0.00	0.00
CON-LEG101-PR-4000	Material Delivery for Backfilling Materials	21	1,529,448.00	02-Feb-26	26-Feb-26	01-Dec-25	31-Mar-26	1,529,448.00	1,529,448.00	1.00
Aggregate Base Course		99	298,440.00	12-Jan-26	14-Jun-26	20-Dec-25	21-May-26	298,440.00	298,440.00	1.00
CON-LEG101-PR-1470	PO for Aggregate Base Course	5	0.00	12-Jan-26	17-Jan-26	20-Dec-25	20-Dec-25	0.00	0.00	0.00
CON-LEG101-PR-1490	Material Delivery for Aggregate Base Course	21	298,440.00	17-May-26	14-Jun-26	15-Jan-26	21-May-26	298,440.00	298,440.00	1.00
Precast Concrete Kerb		295	676,820.00	12-Jan-26	06-Dec-26	01-Feb-26	23-Jul-26	0.00	676,820.00	0.00
CON-LEG101-PR-1520	PO for Precast Concrete Kerb	5	0.00	12-Jan-26	17-Jan-26	01-Feb-26	02-Feb-26	0.00	0.00	0.00
CON-LEG101-PR-1540	Material Delivery for Precast Concrete Kerb	21	676,820.00	12-Nov-26	06-Dec-26	02-May-26	23-Jul-26	0.00	676,820.00	0.00
Interlocking Block Pavers		234	849,240.00	12-Jan-26	06-Dec-26	11-Jun-26	30-Jul-26	0.00	849,240.00	0.00
CON-LEG101-PR-1550	PO for Interlocking Block Pavers	5	0.00	12-Jan-26	17-Jan-26	11-Jun-26	11-Jun-26	0.00	0.00	0.00
CON-LEG101-PR-1570	Material Delivery for Interlocking Block Pavers	21	849,240.00	12-Nov-26	06-Dec-26	13-Jun-26	30-Jul-26	0.00	849,240.00	0.00
Water Proofing		54	70,590.00	06-Jan-26	15-Mar-26	03-Jan-26	05-Mar-26	70,590.00	70,590.00	1.00
CON-LEG101-PR-1440	PO for Water Proofing	5	0.00	06-Jan-26	11-Jan-26	03-Jan-26	03-Jan-26	0.00	0.00	0.00
CON-LEG101-PR-1460	Material Delivery for Water Proofing	21	70,590.00	18-Feb-26	15-Mar-26	03-Jan-26	05-Mar-26	70,590.00	70,590.00	1.00
Handicap ramp		354	34,800.00	12-Jan-26	30-Mar-27	02-Apr-26	10-Jun-26	0.00	34,800.00	0.00
CON-LEG101-PR-2580	PO for Handicap ramp	5	0.00	12-Jan-26	17-Jan-26	02-Apr-26	02-Apr-26	0.00	0.00	0.00
CON-LEG101-PR-2600	Material Delivery for Handicap ramp	15	34,800.00	14-Mar-27	30-Mar-27	10-Jun-26	10-Jun-26	0.00	34,800.00	0.00
Pavement Markings		423	35,820.00	12-Jan-26	04-Apr-27	02-Apr-26		0.00	0.00	0.00
CON-LEG101-PR-1580	PO for Pavement Markings	5	0.00	12-Jan-26	17-Jan-26	02-Apr-26	02-Apr-26	0.00	0.00	0.00
CON-LEG101-PR-1600	Material Delivery for Pavement Markings	15	35,820.00	14-Mar-27	30-Mar-27			0.00	0.00	0.00
CON-LEG101-PR-2070	Staging Time for Pavement Markings	4	0.00	31-Mar-27	04-Apr-27			0.00	0.00	0.00
Bituminous Base & Wearing Course		465	1,672,040.00	12-Jan-26	06-Apr-27	20-Dec-25		961,640.00	1,480,232.00	1.54
CON-LEG101-PR-1500	PO for Bituminous Base & Wearing Course	5	0.00	12-Jan-26	17-Jan-26	20-Dec-25	20-Dec-25	0.00	0.00	0.00
CON-LEG101-PR-1510	Material Delivery for Bituminous Base Course	21	961,640.00	15-Jun-26	08-Jul-26	19-May-26	11-Aug-26	961,640.00	961,640.00	1.00
CON-LEG101-PR-1530	Material Delivery for Wearing Course	21	710,400.00	14-Mar-27	06-Apr-27	29-Sep-26		0.00	518,592.00	0.00
Long Lead Item		498	10,419,329.00	30-Dec-25	14-Sep-27	09-Dec-25		8,905,932.00	9,213,879.00	1.03
Sanitary Sewerage		92	1,137,100.00	31-Dec-25	16-May-26	17-Dec-25	13-Apr-26	1,137,100.00	1,137,100.00	1.00
GRP Pipes		87	705,900.00	31-Dec-25	05-May-26	17-Dec-25	13-Apr-26	705,900.00	705,900.00	1.00
CON-LEG101-PR-1700	PO for GRP Pipes for Sewer network	3	0.00	31-Dec-25	03-Jan-26	17-Dec-25	17-Dec-25	0.00	0.00	0.00
CON-LEG101-PR-1710	Material Fabrication for GRP Pipes for Sewer network	75	0.00	04-Jan-26	06-Apr-26	18-Dec-25	15-Mar-26	0.00	0.00	0.00
CON-LEG101-PR-1720	Material Delivery for GRP Pipes for Sewer network	15	705,900.00	07-Apr-26	23-Apr-26	29-Dec-25	12-Apr-26	705,900.00	705,900.00	1.00
CON-LEG101-PR-2560	Staging Time for GRP Pipes for Sewer network	10	0.00	25-Apr-26	05-May-26	30-Dec-25	13-Apr-26	0.00	0.00	0.00
Fiberglass Manholes		80	431,200.00	08-Jan-26	16-May-26	29-Dec-25	04-Apr-26	431,200.00	431,200.00	1.00
CON-LEG101-PR-1730	PO for Fiberglass Manholes for Sewer network	5	0.00	08-Jan-26	13-Jan-26	29-Dec-25	30-Dec-25	0.00	0.00	0.00
CON-LEG101-PR-1740	Material Fabrication for Fiberglass Manholes for Sewer network	75	0.00	14-Jan-26	16-Apr-26	31-Dec-25	28-Jan-26	0.00	0.00	0.00
CON-LEG101-PR-1750	Material Delivery for Fiberglass Manholes for Sewer network	15	431,200.00	18-Apr-26	04-May-26	20-Jan-26	02-Apr-26	431,200.00	431,200.00	1.00
CON-LEG101-PR-2570	Staging Time for Fiberglass Manholes for Sewer network	10	0.00	05-May-26	16-May-26	20-Jan-26	04-Apr-26	0.00	0.00	0.00
TSE Network		194	1,162,550.00	06-Jan-26	30-Aug-26	01-Jan-26	23-Apr-26	1,162,550.00	1,162,550.00	1.00
HDPE Pipe (PN 16)		96	631,650.00	06-Jan-26	08-Jun-26	01-Jan-26	01-Apr-26	631,650.00	631,650.00	1.00
CON-LEG101-PR-1670	PO for HDPE Pipe (PN 16) for TSE	5	0.00	06-Jan-26	11-Jan-26	01-Jan-26	01-Jan-26	0.00	0.00	0.00
CON-LEG101-PR-1680	Material Fabrication for HDPE Pipe (PN 16) for TSE	75	0.00	12-Jan-26	14-Apr-26	03-Jan-26	25-Mar-26	0.00	0.00	0.00
CON-LEG101-PR-1690	Material Delivery for HDPE Pipe (PN 16) for TSE	15	631,650.00	06-May-26	23-May-26	04-Jan-26	31-Mar-26	631,650.00	631,650.00	1.00
CON-LEG101-PR-2590	Staging Time for HDPE Pipe (PN 16) for TSE	10	0.00	24-May-26	08-Jun-26	05-Jan-26	01-Apr-26	0.00	0.00	0.00
Valves		120	370,700.00	13-Jan-26	07-Jul-26	28-Jan-26	29-Mar-26	370,700.00	370,700.00	1.00
CON-LEG101-PR-1360	PO for Valves for TSE	5	0.00	13-Jan-26	18-Jan-26	28-Jan-26	28-Jan-26	0.00	0.00	0.00
CON-LEG101-PR-1370	Material Fabrication for Valves for TSE	90	0.00	19-Jan-26	09-May-26	29-Jan-26	02-Feb-26	0.00	0.00	0.00
CON-LEG101-PR-1380	Material Delivery for Valves for TSE	15	370,700.00	09-Jun-26	25-Jun-26	03-Feb-26	28-Mar-26	370,700.00	370,700.00	1.00
CON-LEG101-PR-1970	Staging Time for Valves for TSE	10	0.00	27-Jun-26	07-Jul-26	04-Feb-26	29-Mar-26	0.00	0.00	0.00

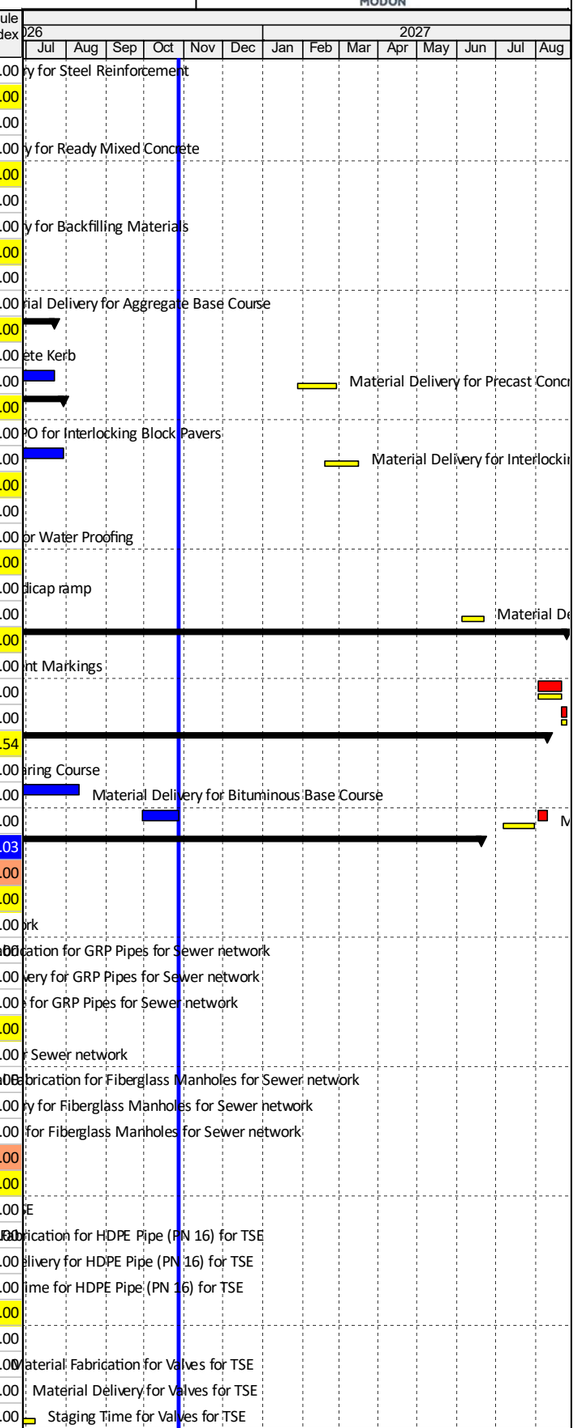


© Oracle Corporation

Activity ID	Activity Name	Original Duration	Budgeted Total Cost	BL Project Start	BL Project Finish	Actual Start	Actual Finish	Planned Value Cost	Earned Value Cost	Schedule Performance Index
Fire Hydrant		167	160,200.00	12-Jan-26	30-Aug-26	28-Jan-26	23-Apr-26	160,200.00	160,200.00	1.00
CON-LEG101-PR-2440	PO for Fire Hydrant	3	0.00	12-Jan-26	14-Jan-26	28-Jan-26	28-Jan-26	0.00	0.00	0.00
CON-LEG101-PR-2450	Material Fabrication for Fire Hydrant	120	0.00	28-Feb-26	26-Jul-26	29-Jan-26	02-Feb-26	0.00	0.00	0.00
CON-LEG101-PR-2460	Material Delivery for Fire Hydrant	20	160,200.00	27-Jul-26	18-Aug-26	03-Feb-26	22-Apr-26	160,200.00	160,200.00	1.00
CON-LEG101-PR-2470	Staging Time for Fire Hydrant	10	0.00	19-Aug-26	30-Aug-26	04-Feb-26	23-Apr-26	0.00	0.00	0.00
Stormwater Utilities		136	2,083,132.00	30-Dec-25	21-Jun-26	09-Dec-25	13-Apr-26	2,083,132.00	2,083,132.00	1.00
GRP Pipes		81	943,530.00	31-Dec-25	04-May-26	09-Dec-25	13-Apr-26	943,530.00	943,530.00	1.00
CON-LEG101-PR-1790	PO for GRP Pipes for Storm network	3	0.00	31-Dec-25	03-Jan-26	09-Dec-25	09-Dec-25	0.00	0.00	0.00
CON-LEG101-PR-1800	Material Fabrication for GRP Pipes for Storm network	75	0.00	04-Jan-26	06-Apr-26	10-Dec-25	12-Mar-26	0.00	0.00	0.00
CON-LEG101-PR-1810	Material Delivery for GRP Pipes for Storm network	14	943,530.00	07-Apr-26	22-Apr-26	16-Dec-25	12-Apr-26	943,530.00	943,530.00	1.00
CON-LEG101-PR-2100	Staging Time for GRP Pipes for Storm network	10	0.00	23-Apr-26	04-May-26	20-Dec-25	13-Apr-26	0.00	0.00	0.00
UPVC Pipes		103	303,902.00	30-Dec-25	04-May-26	28-Jan-26	02-Apr-26	303,902.00	303,902.00	1.00
CON-LEG101-PR-1760	PO for UPVC Pipes	3	0.00	30-Dec-25	01-Jan-26	28-Jan-26	28-Jan-26	0.00	0.00	0.00
CON-LEG101-PR-1770	Material Fabrication for UPVC Pipes	75	0.00	03-Jan-26	05-Apr-26	29-Jan-26	29-Mar-26	0.00	0.00	0.00
CON-LEG101-PR-1780	Material Delivery for UPVC Pipes	15	303,902.00	06-Apr-26	22-Apr-26	31-Jan-26	01-Apr-26	303,902.00	303,902.00	1.00
CON-LEG101-PR-2110	Staging Time for UPVC Pipes	10	0.00	23-Apr-26	04-May-26	01-Feb-26	02-Apr-26	0.00	0.00	0.00
Inlet Manholes		78	489,100.00	05-Jan-26	06-May-26	17-Dec-25	04-Apr-26	489,100.00	489,100.00	1.00
CON-LEG101-PR-1820	PO for Inlet Manholes for Storm network	5	0.00	05-Jan-26	10-Jan-26	17-Dec-25	17-Dec-25	0.00	0.00	0.00
CON-LEG101-PR-1830	Material Fabrication for Inlet Manholes for Storm network	70	0.00	11-Jan-26	07-Apr-26	18-Dec-25	28-Jan-26	0.00	0.00	0.00
CON-LEG101-PR-1840	Material Delivery for Inlet Manholes for Storm network	15	489,100.00	08-Apr-26	25-Apr-26	28-Dec-25	02-Apr-26	489,100.00	489,100.00	1.00
CON-LEG101-PR-1980	Staging Time for Inlet Manholes for Storm network	10	0.00	26-Apr-26	06-May-26	30-Dec-25	04-Apr-26	0.00	0.00	0.00
Concrete chambers		94	346,600.00	13-Jan-26	21-Jun-26	23-Dec-25	09-Apr-26	346,600.00	346,600.00	1.00
CON-LEG101-PR-1850	PO for Concrete chambers	3	0.00	13-Jan-26	15-Jan-26	23-Dec-25	23-Dec-25	0.00	0.00	0.00
CON-LEG101-PR-1860	Material Fabrication for Concrete chambers	75	0.00	28-Jan-26	30-Apr-26	27-Dec-25	02-Apr-26	0.00	0.00	0.00
CON-LEG101-PR-1870	Material Delivery for Concrete chambers	20	346,600.00	02-May-26	24-May-26	31-Jan-26	08-Apr-26	346,600.00	346,600.00	1.00
CON-LEG101-PR-1990	Staging Time for Concrete chambers	20	0.00	25-May-26	21-Jun-26	01-Feb-26	09-Apr-26	0.00	0.00	0.00
Public Water Utility Distribution		172	988,424.00	07-Jan-26	05-Aug-26	01-Jan-26	04-Apr-26	988,424.00	988,424.00	1.00
HDPE Pipe (PN 16)		83	737,624.00	07-Jan-26	12-May-26	01-Jan-26	04-Apr-26	737,624.00	737,624.00	1.00
CON-LEG101-PR-1640	PO for HDPE Pipe (PN 16) for Ptable Water	3	0.00	07-Jan-26	10-Jan-26	01-Jan-26	01-Jan-26	0.00	0.00	0.00
CON-LEG101-PR-1650	Material Fabrication for HDPE Pipe (PN 16) for Ptable Water	75	0.00	11-Jan-26	13-Apr-26	03-Jan-26	25-Mar-26	0.00	0.00	0.00
CON-LEG101-PR-1660	Material Delivery for HDPE Pipe (PN 16) for Ptable Water	15	737,624.00	14-Apr-26	30-Apr-26	04-Jan-26	02-Apr-26	737,624.00	737,624.00	1.00
CON-LEG101-PR-4010	Staging Time for HDPE Pipe (PN 16) for Ptable Water	10	0.00	02-May-26	12-May-26	05-Jan-26	04-Apr-26	0.00	0.00	0.00
Valves		145	250,800.00	12-Jan-26	05-Aug-26	28-Jan-26	29-Mar-26	250,800.00	250,800.00	1.00
CON-LEG101-PR-1330	PO for Valves for Ptable Water	5	0.00	12-Jan-26	17-Jan-26	28-Jan-26	28-Jan-26	0.00	0.00	0.00
CON-LEG101-PR-1340	Material Fabrication for Valves for Ptable Water	90	0.00	28-Jan-26	18-May-26	29-Jan-26	02-Feb-26	0.00	0.00	0.00
CON-LEG101-PR-1350	Material Delivery for Valves for Ptable Water	15	250,800.00	08-Jul-26	25-Jul-26	03-Feb-26	28-Mar-26	250,800.00	250,800.00	1.00
CON-LEG101-PR-1960	Staging Time for Valves for Ptable Water	10	0.00	26-Jul-26	05-Aug-26	04-Feb-26	29-Mar-26	0.00	0.00	0.00
Fence & Gates		323	952,504.00	01-Jan-26	20-Aug-26	27-Dec-25		952,504.00	921,304.00	0.97
Metal Fence		134	872,560.00	01-Jan-26	09-May-26	27-Dec-25	30-Jul-26	872,560.00	872,560.00	1.00
CON-LEG101-PR-2000	PO for Metal Fence	5	0.00	01-Jan-26	06-Jan-26	27-Dec-25	27-Dec-25	0.00	0.00	0.00
CON-LEG101-PR-2010	Material Fabrication for Metal Fence	75	0.00	07-Jan-26	09-Apr-26	28-Dec-25	08-Jun-26	0.00	0.00	0.00
CON-LEG101-PR-2020	Material Delivery for Metal Fence	15	872,560.00	11-Apr-26	27-Apr-26	10-Mar-26	28-Jul-26	872,560.00	872,560.00	1.00
CON-LEG101-PR-2080	Staging Time for Metal Fence	10	0.00	28-Apr-26	09-May-26	11-Mar-26	30-Jul-26	0.00	0.00	0.00
Gates		323	31,200.00	05-Jan-26	20-Aug-26	27-Dec-25		31,200.00	0.00	0.00
CON-LEG101-PR-2030	PO for Gates	5	0.00	05-Jan-26	10-Jan-26	27-Dec-25	27-Dec-25	0.00	0.00	0.00
CON-LEG101-PR-2040	Material Fabrication for Gates	70	0.00	28-Apr-26	22-Jul-26	28-Dec-25		0.00	0.00	0.00
CON-LEG101-PR-2050	Material Delivery for Gates	15	31,200.00	23-Jul-26	09-Aug-26			31,200.00	0.00	0.00
CON-LEG101-PR-2090	Staging Time for Gates	10	0.00	10-Aug-26	20-Aug-26			0.00	0.00	0.00
Paint On Cement Plaster		118	48,744.00	11-Jan-26	10-Jun-26	13-Jan-26	16-Apr-26	48,744.00	48,744.00	1.00
CON-LEG101-PR-2610	PO for Paint On Cement Plaster	5	0.00	11-Jan-26	15-Jan-26	13-Jan-26	13-Jan-26	0.00	0.00	0.00
CON-LEG101-PR-2620	Material Fabrication for Paint On Cement Plaster	30	0.00	11-Apr-26	14-May-26	09-Apr-26	12-Apr-26	0.00	0.00	0.00
CON-LEG101-PR-2630	Material Delivery for Paint On Cement Plaster	10	48,744.00	16-May-26	26-May-26	15-Apr-26	15-Apr-26	48,744.00	48,744.00	1.00
CON-LEG101-PR-2940	Staging Time for Paint On Cement Plaster	9	0.00	01-Jun-26	10-Jun-26	16-Apr-26	16-Apr-26	0.00	0.00	0.00

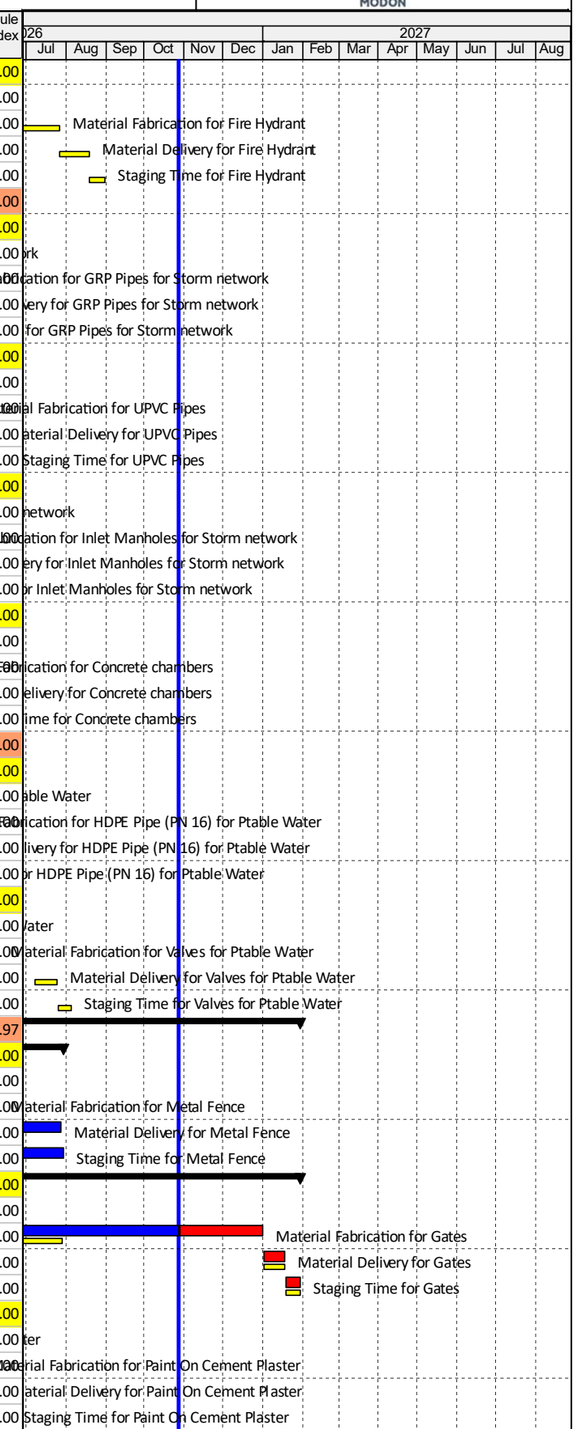


© Oracle Corporation

Activity ID	Activity Name	Original Duration	Budgeted Total Cost	BL Project Start	BL Project Finish	Actual Start	Actual Finish	Planned Value Cost	Earned Value Cost	Schedule Performance Index
Telecommunications		238	736,322.00	04-Jan-26	02-Dec-26	08-Feb-26	26-Apr-26	471,770.00	736,322.00	1.56
Pipe for the Duct		227	460,762.00	04-Jan-26	08-Oct-26	15-Feb-26	30-Mar-26	460,762.00	460,762.00	1.00
CON-LEG101-PR-3160	PO for Pipe for Duct	5	0.00	04-Jan-26	08-Jan-26	15-Feb-26	15-Feb-26	0.00	0.00	0.00
CON-LEG101-PR-3170	Material Fabrication for Pipe for Duct	55	0.00	01-Jul-26	02-Sep-26	17-Feb-26	05-Mar-26	0.00	0.00	0.00
CON-LEG101-PR-3180	Material Delivery for Pipe for Duct	15	460,762.00	03-Sep-26	20-Sep-26	21-Feb-26	30-Mar-26	460,762.00	460,762.00	1.00
CON-LEG101-PR-4020	Staging Time for Pipe for Duct	15	0.00	21-Sep-26	08-Oct-26	22-Feb-26	30-Mar-26	0.00	0.00	0.00
Low Voltage Cables		231	13,760.00	11-Jan-26	24-Nov-26	08-Feb-26	16-Apr-26	11,008.00	13,760.00	1.25
CON-LEG101-PR-3190	PO for Low Voltage Cables	5	0.00	11-Jan-26	15-Jan-26	08-Feb-26	08-Feb-26	0.00	0.00	0.00
CON-LEG101-PR-3210	Material Fabrication for Low Voltage Cables	55	0.00	01-Jul-26	02-Sep-26	10-Feb-26	09-Apr-26	0.00	0.00	0.00
CON-LEG101-PR-3230	Material Delivery for Low Voltage Cables	20	13,760.00	10-Oct-26	01-Nov-26	14-Mar-26	15-Apr-26	11,008.00	13,760.00	1.25
CON-LEG101-PR-3250	Staging Time for Low Voltage Cables	20	0.00	02-Nov-26	24-Nov-26	15-Mar-26	16-Apr-26	0.00	0.00	0.00
Manhole		230	261,800.00	13-Jan-26	02-Dec-26	18-Feb-26	26-Apr-26	0.00	261,800.00	0.00
CON-LEG101-PR-3200	PO for Manhole	5	0.00	13-Jan-26	18-Jan-26	18-Feb-26	19-Feb-26	0.00	0.00	0.00
CON-LEG101-PR-3220	Material Fabrication for Manhole	75	0.00	01-Jul-26	27-Sep-26	21-Feb-26	20-Apr-26	0.00	0.00	0.00
CON-LEG101-PR-3240	Material Delivery for Manhole	15	261,800.00	02-Nov-26	18-Nov-26	15-Mar-26	25-Apr-26	0.00	261,800.00	0.00
CON-LEG101-PR-3260	Staging Time for Manhole	12	0.00	19-Nov-26	02-Dec-26	16-Mar-26	26-Apr-26	0.00	0.00	0.00
Road Works - Civil		369	137,260.00	12-Jan-26	04-Jan-27	07-Apr-26	04-Jul-26	0.00	137,260.00	0.00
Traffic Signs		369	137,260.00	12-Jan-26	04-Jan-27	07-Apr-26	04-Jul-26	0.00	137,260.00	0.00
CON-LEG101-PR-1610	PO for Traffic Signs	5	0.00	12-Jan-26	17-Jan-26	07-Apr-26	08-Apr-26	0.00	0.00	0.00
CON-LEG101-PR-1620	Material Fabrication for Traffic Signs	90	0.00	28-Jan-26	18-May-26	09-Apr-26	01-Jul-26	0.00	0.00	0.00
CON-LEG101-PR-1630	Material Delivery for Traffic Signs	15	137,260.00	07-Dec-26	23-Dec-26	13-Jun-26	02-Jul-26	0.00	137,260.00	0.00
CON-LEG101-PR-2060	Staging Time for Traffic Signs	10	0.00	24-Dec-26	04-Jan-27	14-Jun-26	04-Jul-26	0.00	0.00	0.00
Electrical Network		398	1,827,732.00	04-Jan-26	02-Feb-27	08-Feb-26		1,819,732.00	936,412.00	0.51
Pipe for the Duct		115	107,032.00	04-Jan-26	07-Jun-26	15-Feb-26	31-Mar-26	107,032.00	107,032.00	1.00
CON-LEG101-PR-1260	PO for Pipe for Duct	3	0.00	04-Jan-26	06-Jan-26	15-Feb-26	16-Feb-26	0.00	0.00	0.00
CON-LEG101-PR-1290	Material Fabrication for Pipe for Duct	90	0.00	07-Jan-26	27-Apr-26	16-Feb-26	24-Mar-26	0.00	0.00	0.00
CON-LEG101-PR-1320	Material Delivery for Pipe for Duct	15	107,032.00	05-May-26	21-May-26	25-Feb-26	28-Mar-26	107,032.00	107,032.00	1.00
CON-LEG101-PR-1400	Staging Time for Valves for Pipe for Duct	10	0.00	23-May-26	07-Jun-26	26-Feb-26	31-Mar-26	0.00	0.00	0.00
Cable Termination & Joints		174	39,320.00	11-Jan-26	24-Jun-26	02-Sep-26		39,320.00	0.00	0.00
CON-LEG101-PR-1240	PO for Cable Termination & Joints	5	0.00	11-Jan-26	15-Jan-26	02-Sep-26		0.00	0.00	0.00
CON-LEG101-PR-1270	Material Fabrication for Cable Termination & Joints	90	0.00	28-Jan-26	18-May-26			0.00	0.00	0.00
CON-LEG101-PR-1300	Material Delivery for Cable Termination & Joints	15	39,320.00	23-May-26	13-Jun-26			39,320.00	0.00	0.00
CON-LEG101-PR-1450	Stagging Time for Cable Termination & Joints	10	0.00	14-Jun-26	24-Jun-26			0.00	0.00	0.00
Earthing System		228	35,900.00	11-Jan-26	09-Aug-26	08-Feb-26	10-May-26	35,900.00	35,900.00	1.00
CON-LEG101-PR-1250	PO for Earthing System	5	0.00	11-Jan-26	15-Jan-26	08-Feb-26	09-Feb-26	0.00	0.00	0.00
CON-LEG101-PR-1280	Material Fabrication for Earthing System	60	0.00	28-Apr-26	11-Jul-26	27-Feb-26	05-Mar-26	0.00	0.00	0.00
CON-LEG101-PR-1310	Material Delivery for Earthing System	15	35,900.00	12-Jul-26	28-Jul-26	02-May-26	07-May-26	35,900.00	35,900.00	1.00
CON-LEG101-PR-1480	Stagging Time for Earthing System	10	0.00	29-Jul-26	09-Aug-26	09-May-26	10-May-26	0.00	0.00	0.00
Medium Voltage Cable		164	640,000.00	13-Jan-26	01-Jun-26	02-Sep-26		640,000.00	0.00	0.00
CON-LEG101-PR-1000	PO for Medium Voltage Cable	5	0.00	13-Jan-26	18-Jan-26	02-Sep-26		0.00	0.00	0.00
CON-LEG101-PR-1080	Material Fabrication for Medium Voltage Cable	60	0.00	01-Feb-26	16-Apr-26			0.00	0.00	0.00
CON-LEG101-PR-1160	Material Delivery for Medium Voltage Cable	15	640,000.00	23-Apr-26	10-May-26			640,000.00	0.00	0.00
CON-LEG101-PR-1880	Staging Time for Medium Voltage Cable	15	0.00	11-May-26	01-Jun-26			0.00	0.00	0.00
Street Lighting Sub-station		258	68,000.00	11-Jan-26	07-Sep-26	05-Apr-26		68,000.00	0.00	0.00
CON-LEG101-PR-1010	PO for Street Lighting Sub-station	5	0.00	11-Jan-26	15-Jan-26	05-Apr-26	05-Apr-26	0.00	0.00	0.00
CON-LEG101-PR-1090	Material Fabrication for Street Lighting Sub-station	60	0.00	18-Apr-26	30-Jun-26			0.00	0.00	0.00
CON-LEG101-PR-1170	Material Delivery for Street Lighting Sub-station	15	68,000.00	10-Aug-26	26-Aug-26			68,000.00	0.00	0.00
CON-LEG101-PR-1890	Staging Time for Street Lighting Sub-station	10	0.00	27-Aug-26	07-Sep-26			0.00	0.00	0.00
Low Voltage Cables		204	309,640.00	07-Jan-26	26-Sep-26	08-Feb-26	16-Apr-26	309,640.00	309,640.00	1.00
CON-LEG101-PR-1020	PO for Low Voltage Cables	5	0.00	07-Jan-26	12-Jan-26	08-Feb-26	09-Feb-26	0.00	0.00	0.00
CON-LEG101-PR-1100	Material Fabrication for Low Voltage Cables	60	0.00	18-Apr-26	30-Jun-26	11-Feb-26	09-Apr-26	0.00	0.00	0.00
CON-LEG101-PR-1180	Material Delivery for Low Voltage Cables	15	309,640.00	27-Aug-26	13-Sep-26	14-Mar-26	15-Apr-26	309,640.00	309,640.00	1.00
CON-LEG101-PR-1900	Staging Time for Low Voltage Cables	10	0.00	14-Sep-26	26-Sep-26	15-Mar-26	16-Apr-26	0.00	0.00	0.00

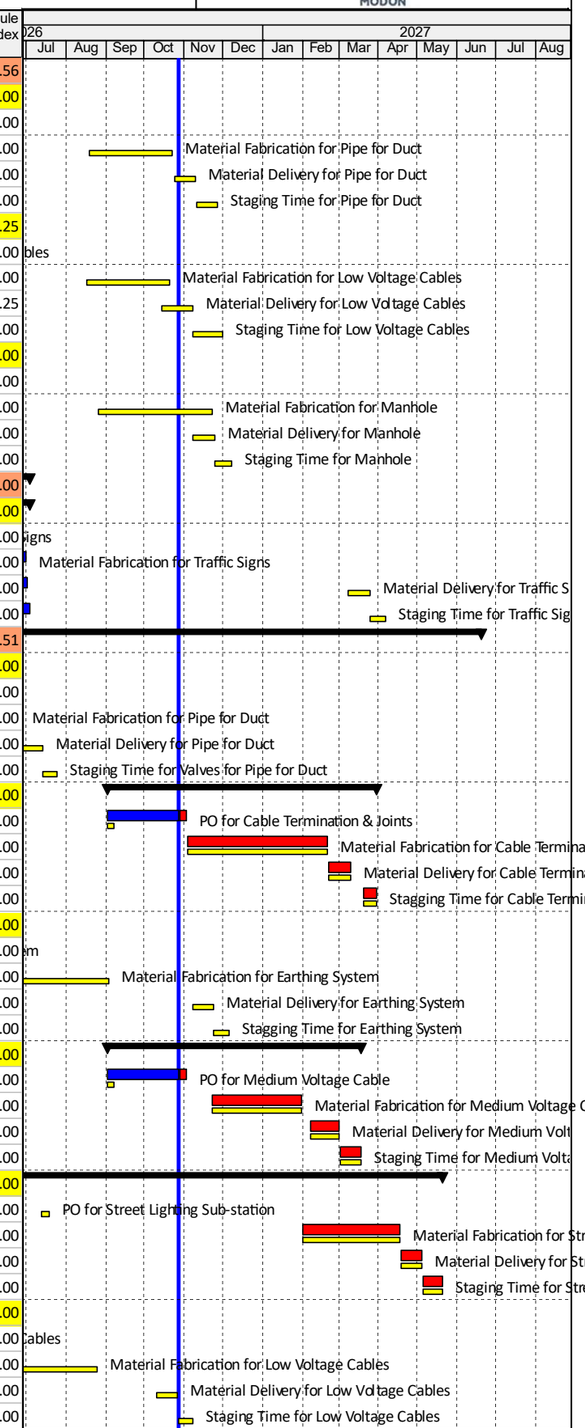


© Oracle Corporation

Activity ID	Activity Name	Original Duration	Budgeted Total Cost	BL Project Start	BL Project Finish	Actual Start	Actual Finish	Planned Value Cost	Earned Value Cost	Schedule Performance Index
Ring Main Unit		188	144,000.00	11-Jan-26	25-Oct-26			144,000.00	0.00	0.00
CON-LEG101-PR-2480	PO for Ring Main Unit	5	0.00	11-Jan-26	15-Jan-26			0.00	0.00	0.00
CON-LEG101-PR-2490	Material Fabrication for Ring Main Unit	70	0.00	01-Jul-26	20-Sep-26			0.00	0.00	0.00
CON-LEG101-PR-2500	Material Delivery for Ring Main Unit	15	144,000.00	27-Sep-26	13-Oct-26			144,000.00	0.00	0.00
CON-LEG101-PR-2510	Staging Time for Ring Main Unit	10	0.00	14-Oct-26	25-Oct-26			0.00	0.00	0.00
Lighting poles		199	301,240.00	13-Jan-26	10-Sep-26	16-Feb-26	13-Apr-26	301,240.00	301,240.00	1.00
CON-LEG101-PR-1030	PO for Lighting poles	4	0.00	13-Jan-26	17-Jan-26	16-Feb-26	16-Feb-26	0.00	0.00	0.00
CON-LEG101-PR-1110	Material Fabrication for Lighting poles	75	0.00	11-May-26	10-Aug-26	17-Feb-26	31-Mar-26	0.00	0.00	0.00
CON-LEG101-PR-1190	Material Delivery for Lighting poles	15	301,240.00	11-Aug-26	27-Aug-26	01-Apr-26	12-Apr-26	301,240.00	301,240.00	1.00
CON-LEG101-PR-1910	Staging Time for Lighting poles	12	0.00	29-Aug-26	10-Sep-26	02-Apr-26	13-Apr-26	0.00	0.00	0.00
Lighting panels		219	0.00	11-Jan-26	05-Nov-26	05-Apr-26	12-Aug-26	0.00	0.00	0.00
CON-LEG101-PR-2520	PO for Lighting panels	6	0.00	11-Jan-26	17-Jan-26	05-Apr-26	05-Apr-26	0.00	0.00	0.00
CON-LEG101-PR-2530	Material Fabrication for Lighting panels	75	0.00	01-Jul-26	27-Sep-26	02-May-26	06-Aug-26	0.00	0.00	0.00
CON-LEG101-PR-2540	Material Delivery for Lighting panels	15	0.00	28-Sep-26	14-Oct-26	08-Aug-26	10-Aug-26	0.00	0.00	0.00
CON-LEG101-PR-2550	Staging Time for Lighting panels	10	0.00	26-Oct-26	05-Nov-26	12-Aug-26	12-Aug-26	0.00	0.00	0.00
Street Lighting Luminaire		199	88,600.00	13-Jan-26	10-Sep-26	16-Feb-26	13-Apr-26	88,600.00	88,600.00	1.00
CON-LEG101-PR-1040	PO for Street Lighting Luminaire	4	0.00	13-Jan-26	17-Jan-26	16-Feb-26	16-Feb-26	0.00	0.00	0.00
CON-LEG101-PR-1120	Material Fabrication for Street Lighting Luminaire	75	0.00	11-May-26	10-Aug-26	17-Feb-26	31-Mar-26	0.00	0.00	0.00
CON-LEG101-PR-1200	Material Delivery for Street Lighting Luminaire	15	88,600.00	11-Aug-26	27-Aug-26	01-Apr-26	12-Apr-26	88,600.00	88,600.00	1.00
CON-LEG101-PR-1920	Staging Time for Street Lighting Luminaire	12	0.00	29-Aug-26	10-Sep-26	02-Apr-26	13-Apr-26	0.00	0.00	0.00
System for KWHM		250	8,000.00	11-Jan-26	02-Feb-27	16-Jul-26	12-Aug-26	0.00	8,000.00	0.00
CON-LEG101-PR-1050	PO for System for KWHM	6	0.00	11-Jan-26	17-Jan-26	16-Jul-26	16-Jul-26	0.00	0.00	0.00
CON-LEG101-PR-1130	Material Fabrication for System for KWHM	90	0.00	21-Sep-26	04-Jan-27	18-Jul-26	06-Aug-26	0.00	0.00	0.00
CON-LEG101-PR-1210	Material Delivery for System for KWHM	15	8,000.00	05-Jan-27	21-Jan-27	08-Aug-26	10-Aug-26	0.00	8,000.00	0.00
CON-LEG101-PR-1930	Staging Time for System for KWHM	10	0.00	23-Jan-27	02-Feb-27	11-Aug-26	12-Aug-26	0.00	0.00	0.00
Feeder Piller		105	70,000.00	11-Jan-26	01-Nov-26	16-Jul-26	12-Aug-26	70,000.00	70,000.00	1.00
CON-LEG101-PR-1060	PO for Feeder Piller	6	0.00	11-Jan-26	17-Jan-26	16-Jul-26	16-Jul-26	0.00	0.00	0.00
CON-LEG101-PR-1140	Material Fabrication for Feeder Piller	75	0.00	01-Jul-26	27-Sep-26	18-Jul-26	06-Aug-26	0.00	0.00	0.00
CON-LEG101-PR-1220	Material Delivery for Feeder Piller	15	70,000.00	28-Sep-26	14-Oct-26	08-Aug-26	10-Aug-26	70,000.00	70,000.00	1.00
CON-LEG101-PR-1940	Staging Time for Feeder Piller	15	0.00	15-Oct-26	01-Nov-26	11-Aug-26	12-Aug-26	0.00	0.00	0.00
Street Lighting Panels		105	16,000.00	11-Jan-26	26-Oct-26	16-Jul-26	12-Aug-26	16,000.00	16,000.00	1.00
CON-LEG101-PR-1070	PO for Street Lighting Panels	6	0.00	11-Jan-26	17-Jan-26	16-Jul-26	16-Jul-26	0.00	0.00	0.00
CON-LEG101-PR-1150	Material Fabrication for Street Lighting Panels	75	0.00	01-Jul-26	27-Sep-26	18-Jul-26	06-Aug-26	0.00	0.00	0.00
CON-LEG101-PR-1230	Material Delivery for Street Lighting Panels	15	16,000.00	28-Sep-26	14-Oct-26	08-Aug-26	10-Aug-26	16,000.00	16,000.00	1.00
CON-LEG101-PR-1950	Staging Time for Street Lighting Panels	10	0.00	15-Oct-26	26-Oct-26	11-Aug-26	12-Aug-26	0.00	0.00	0.00
CCTV feeding system and GSM		295	442,840.00	11-Jan-26	11-Mar-27	30-Mar-26	10-Jun-26	109,120.00	442,840.00	4.06
LED Screen 43" (24/7 operation) with Ethernet decoders		295	12,000.00	13-Jan-26	12-Dec-26	30-Mar-26	10-Jun-26	0.00	12,000.00	0.00
CON-LEG101-PR-3270	PO for LED Screen 43" (24/7 operation) with Ethernet decoders	5	0.00	13-Jan-26	18-Jan-26	30-Mar-26	30-Mar-26	0.00	0.00	0.00
CON-LEG101-PR-3280	Material Fabrication for LED Screen 43" (24/7 operation) with Ethernet	60	0.00	03-Sep-26	12-Nov-26	04-Apr-26	04-Jun-26	0.00	0.00	0.00
CON-LEG101-PR-3290	Material Delivery for LED Screen 43" (24/7 operation) with Ethernet de	15	12,000.00	14-Nov-26	30-Nov-26	10-Jun-26	10-Jun-26	0.00	12,000.00	0.00
CON-LEG101-PR-3950	Staging Time for LED Screen 43" (24/7 operation) with Ethernet decode	10	0.00	01-Dec-26	12-Dec-26	10-Jun-26	10-Jun-26	0.00	0.00	0.00
Network Video Recorder 4k 64 Channel		251	10,000.00	17-Jan-26	25-Feb-27	30-Mar-26	10-Jun-26	0.00	10,000.00	0.00
CON-LEG101-PR-3740	PO for Network Video Recorder 4k 64 Channel	2	0.00	17-Jan-26	18-Jan-26	30-Mar-26	30-Mar-26	0.00	0.00	0.00
CON-LEG101-PR-3750	Material Fabrication for Network Video Recorder 4k 64 Channel	65	0.00	14-Nov-26	27-Jan-27	04-Apr-26	04-Jun-26	0.00	0.00	0.00
CON-LEG101-PR-3760	Material Delivery for Network Video Recorder 4k 64 Channel	10	10,000.00	28-Jan-27	08-Feb-27	10-Jun-26	10-Jun-26	0.00	10,000.00	0.00
CON-LEG101-PR-3960	Staging Time for Network Video Recorder 4k 64 Channel	10	0.00	14-Feb-27	25-Feb-27	10-Jun-26	10-Jun-26	0.00	0.00	0.00
Keypad		261	20,000.00	17-Jan-26	11-Mar-27	30-Mar-26	10-Jun-26	0.00	20,000.00	0.00
CON-LEG101-PR-3770	PO for Keypad	2	0.00	17-Jan-26	18-Jan-26	30-Mar-26	30-Mar-26	0.00	0.00	0.00
CON-LEG101-PR-3780	Material Fabrication for Keypad	75	0.00	14-Nov-26	08-Feb-27	04-Apr-26	04-Jun-26	0.00	0.00	0.00
CON-LEG101-PR-3790	Material Delivery for Keypad	12	20,000.00	14-Feb-27	28-Feb-27	10-Jun-26	10-Jun-26	0.00	20,000.00	0.00
CON-LEG101-PR-3970	Staging Time for Keypad	10	0.00	01-Mar-27	11-Mar-27	10-Jun-26	10-Jun-26	0.00	0.00	0.00
Fiber Optic Patch Panel 12 port		216	17,640.00	11-Jan-26	01-Nov-26	30-Mar-26	10-Jun-26	17,640.00	17,640.00	1.00
CON-LEG101-PR-3300	PO for Fiber Optic Patch Panel 12 port	5	0.00	11-Jan-26	15-Jan-26	30-Mar-26	30-Mar-26	0.00	0.00	0.00

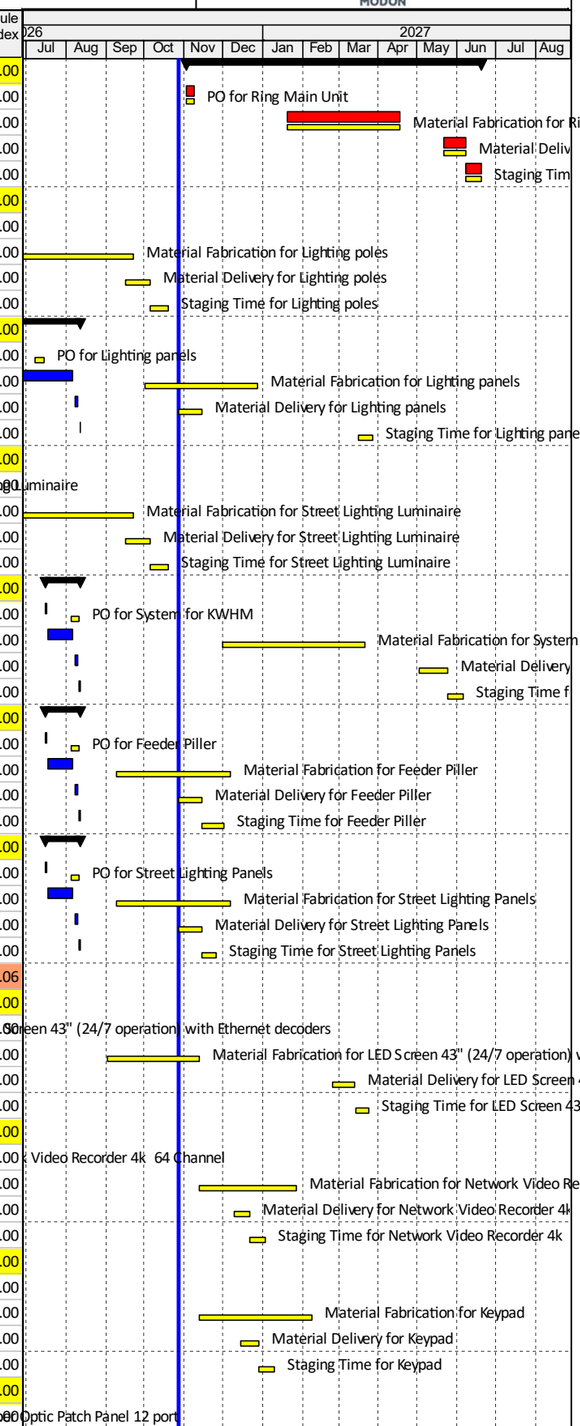

© Oracle Corporation

Activity ID	Activity Name	Original Duration	Budgeted Total Cost	BL Project Start	BL Project Finish	Actual Start	Actual Finish	Planned Value Cost	Earned Value Cost	Schedule Performance Index
CON-LEG101-PR-3320	Material Fabrication for Fiber Optic Patch Panel 12 port	75	0.00	01-Jul-26	27-Sep-26	04-Apr-26	04-Jun-26	0.00	0.00	0.00
CON-LEG101-PR-3340	Material Delivery for Fiber Optic Patch Panel 12 port	15	17,640.00	28-Sep-26	14-Oct-26	10-Jun-26	10-Jun-26	17,640.00	17,640.00	1.00
CON-LEG101-PR-3360	Staging Time for Fiber Optic Patch Panel 12 port	15	0.00	15-Oct-26	01-Nov-26	10-Jun-26	10-Jun-26	0.00	0.00	0.00
Modular Industrial Switches for main pole		246	3,000.00	14-Jan-26	17-Dec-26	30-Mar-26	10-Jun-26	0.00	3,000.00	0.00
CON-LEG101-PR-3310	PO for Modular Industrial Switches for main pole	5	0.00	14-Jan-26	19-Jan-26	30-Mar-26	30-Mar-26	0.00	0.00	0.00
CON-LEG101-PR-3330	Material Fabrication for Modular Industrial Switches for main pole	75	0.00	01-Jul-26	27-Sep-26	04-Apr-26	04-Jun-26	0.00	0.00	0.00
CON-LEG101-PR-3350	Material Delivery for Modular Industrial Switches for main pole	15	3,000.00	02-Nov-26	18-Nov-26	10-Jun-26	10-Jun-26	0.00	3,000.00	0.00
CON-LEG101-PR-3370	Staging Time for Modular Industrial Switches for main pole	15	0.00	01-Dec-26	17-Dec-26	10-Jun-26	10-Jun-26	0.00	0.00	0.00
8POE ports Industrial Switches for remote poles		206	12,000.00	13-Jan-26	07-Nov-26	30-Mar-26	05-May-26	12,000.00	12,000.00	1.00
CON-LEG101-PR-3380	PO for 8POE ports Industrial Switches for remote poles	5	0.00	13-Jan-26	18-Jan-26	30-Mar-26	30-Mar-26	0.00	0.00	0.00
CON-LEG101-PR-3390	Material Fabrication for 8POE ports Industrial Switches for remote pole	70	0.00	01-Jul-26	20-Sep-26	04-Apr-26	30-Apr-26	0.00	0.00	0.00
CON-LEG101-PR-3400	Material Delivery for 8POE ports Industrial Switches for remote poles	20	12,000.00	21-Sep-26	14-Oct-26	02-May-26	04-May-26	12,000.00	12,000.00	1.00
CON-LEG101-PR-3410	Staging Time for 8POE ports Industrial Switches for remote poles	20	0.00	15-Oct-26	07-Nov-26	05-May-26	05-May-26	0.00	0.00	0.00
Core Switch		263	12,000.00	13-Jan-26	16-Jan-27	30-Mar-26	05-May-26	0.00	12,000.00	0.00
CON-LEG101-PR-3420	PO for Core Switch	5	0.00	13-Jan-26	18-Jan-26	30-Mar-26	30-Mar-26	0.00	0.00	0.00
CON-LEG101-PR-3430	Material Fabrication for Core Switch	75	0.00	21-Sep-26	17-Dec-26	04-Apr-26	30-Apr-26	0.00	0.00	0.00
CON-LEG101-PR-3440	Material Delivery for Core Switch	15	12,000.00	19-Dec-26	04-Jan-27	02-May-26	04-May-26	0.00	12,000.00	0.00
CON-LEG101-PR-3450	Staging Time for Core Switch	10	0.00	05-Jan-27	16-Jan-27	05-May-26	05-May-26	0.00	0.00	0.00
Access Switch 48 port		270	6,000.00	13-Jan-26	20-Jan-27	30-Mar-26	05-May-26	0.00	6,000.00	0.00
CON-LEG101-PR-3460	PO for Access Switch 48 port	5	0.00	13-Jan-26	18-Jan-26	30-Mar-26	30-Mar-26	0.00	0.00	0.00
CON-LEG101-PR-3470	Material Fabrication for Access Switch 48 port	75	0.00	30-Sep-26	26-Dec-26	04-Apr-26	30-Apr-26	0.00	0.00	0.00
CON-LEG101-PR-3480	Material Delivery for Access Switch 48 port	15	6,000.00	27-Dec-26	12-Jan-27	02-May-26	04-May-26	0.00	6,000.00	0.00
CON-LEG101-PR-3490	Staging Time for Access Switch 48 port	7	0.00	13-Jan-27	20-Jan-27	05-May-26	05-May-26	0.00	0.00	0.00
Server		208	39,000.00	13-Jan-26	10-Nov-26	30-Mar-26	05-May-26	39,000.00	39,000.00	1.00
CON-LEG101-PR-3500	PO for Server	5	0.00	13-Jan-26	18-Jan-26	30-Mar-26	30-Mar-26	0.00	0.00	0.00
CON-LEG101-PR-3510	Material Fabrication for Server	77	0.00	01-Jul-26	29-Sep-26	04-Apr-26	30-Apr-26	0.00	0.00	0.00
CON-LEG101-PR-3520	Material Delivery for Server	18	39,000.00	30-Sep-26	20-Oct-26	02-May-26	04-May-26	39,000.00	39,000.00	1.00
CON-LEG101-PR-3530	Staging Time for Server	18	0.00	21-Oct-26	10-Nov-26	05-May-26	05-May-26	0.00	0.00	0.00
Stand rack 42U- 19"		270	6,000.00	13-Jan-26	30-Jan-27	30-Mar-26	05-May-26	0.00	6,000.00	0.00
CON-LEG101-PR-3540	PO for Stand rack 42U- 19"	6	0.00	13-Jan-26	19-Jan-26	30-Mar-26	30-Mar-26	0.00	0.00	0.00
CON-LEG101-PR-3550	Material Fabrication for Stand rack 42U- 19"	75	0.00	30-Sep-26	26-Dec-26	04-Apr-26	30-Apr-26	0.00	0.00	0.00
CON-LEG101-PR-3560	Material Delivery for Stand rack 42U- 19"	15	6,000.00	27-Dec-26	12-Jan-27	02-May-26	04-May-26	0.00	6,000.00	0.00
CON-LEG101-PR-3570	Staging Time for Stand rack 42U- 19"	15	0.00	13-Jan-27	30-Jan-27	05-May-26	05-May-26	0.00	0.00	0.00
IP Outdoor CCTV POE Camera,5 MP, Metal Housing		200	28,000.00	13-Jan-26	01-Nov-26	30-Mar-26	05-May-26	28,000.00	28,000.00	1.00
CON-LEG101-PR-3580	PO for IP Outdoor CCTV POE Camera,5 MP, Metal Housing	5	0.00	13-Jan-26	18-Jan-26	30-Mar-26	30-Mar-26	0.00	0.00	0.00
CON-LEG101-PR-3590	Material Fabrication for IP Outdoor CCTV POE Camera,5 MP, Metal Hou	75	0.00	01-Jul-26	27-Sep-26	04-Apr-26	30-Apr-26	0.00	0.00	0.00
CON-LEG101-PR-3600	Material Delivery for IP Outdoor CCTV POE Camera,5 MP, Metal Hou	15	28,000.00	28-Sep-26	14-Oct-26	02-May-26	04-May-26	28,000.00	28,000.00	1.00
CON-LEG101-PR-3610	Staging Time for IP Outdoor CCTV POE Camera,5 MP, Metal Housing	15	0.00	15-Oct-26	01-Nov-26	05-May-26	05-May-26	0.00	0.00	0.00
Outdoor PTZ with IR, HDTV 1080 and 31x optical, 12x digital		225	49,000.00	13-Jan-26	30-Nov-26	30-Mar-26	05-May-26	0.00	49,000.00	0.00
CON-LEG101-PR-3620	PO for Outdoor PTZ with IR, HDTV 1080 and 31x optical, 12x digital	5	0.00	13-Jan-26	18-Jan-26	30-Mar-26	30-Mar-26	0.00	0.00	0.00
CON-LEG101-PR-3630	Material Fabrication for Outdoor PTZ with IR, HDTV 1080 and 31x optic	90	0.00	01-Jul-26	14-Oct-26	04-Apr-26	30-Apr-26	0.00	0.00	0.00
CON-LEG101-PR-3640	Material Delivery for Outdoor PTZ with IR, HDTV 1080 and 31x optical,	15	49,000.00	02-Nov-26	18-Nov-26	02-May-26	04-May-26	0.00	49,000.00	0.00
CON-LEG101-PR-3650	Staging Time for Outdoor PTZ with IR, HDTV 1080 and 31x optical, 12x	10	0.00	19-Nov-26	30-Nov-26	05-May-26	05-May-26	0.00	0.00	0.00
Security workstation with 1 x 19" LED screen		285	5,000.00	13-Jan-26	04-Feb-27	30-Mar-26	05-May-26	0.00	5,000.00	0.00
CON-LEG101-PR-3660	PO for Security workstation with 1 x 19" LED screen	5	0.00	13-Jan-26	18-Jan-26	30-Mar-26	30-Mar-26	0.00	0.00	0.00
CON-LEG101-PR-3670	Material Fabrication for Security workstation with 1 x 19" LED screen	90	0.00	30-Sep-26	12-Jan-27	04-Apr-26	30-Apr-26	0.00	0.00	0.00
CON-LEG101-PR-3680	Material Delivery for Security workstation with 1 x 19" LED screen	10	5,000.00	13-Jan-27	24-Jan-27	02-May-26	04-May-26	0.00	5,000.00	0.00
CON-LEG101-PR-3690	Staging Time for Security workstation with 1 x 19" LED screen	10	0.00	25-Jan-27	04-Feb-27	05-May-26	05-May-26	0.00	0.00	0.00
Horizontal Power Distribution Unit (min 8 outlets)		285	4,000.00	13-Jan-26	28-Feb-27	30-Mar-26	05-May-26	0.00	4,000.00	0.00
CON-LEG101-PR-3700	PO for Horizontal Power Distribution Unit (min 8 outlets)	5	0.00	13-Jan-26	18-Jan-26	30-Mar-26	30-Mar-26	0.00	0.00	0.00
CON-LEG101-PR-3710	Material Fabrication for Horizontal Power Distribution Unit (min 8 outle	90	0.00	30-Sep-26	12-Jan-27	04-Apr-26	30-Apr-26	0.00	0.00	0.00
CON-LEG101-PR-3720	Material Delivery for Horizontal Power Distribution Unit (min 8 outlets)	20	4,000.00	13-Jan-27	04-Feb-27	02-May-26	04-May-26	0.00	4,000.00	0.00
CON-LEG101-PR-3730	Staging Time for Horizontal Power Distribution Unit (min 8 outlets)	15	0.00	06-Feb-27	28-Feb-27	02-May-26	05-May-26	0.00	0.00	0.00

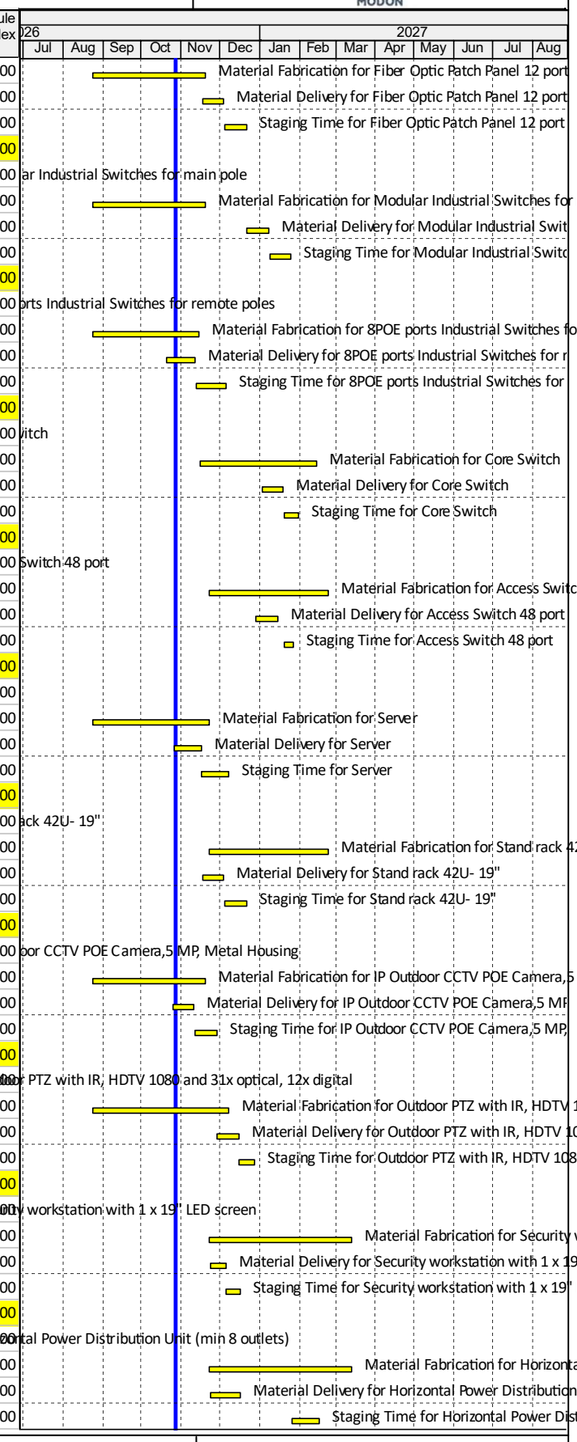


© Oracle Corporation

JDH1-02-003 - Infrastructure Development For Industrial City 1 In Jeddah - Update - 27.10.2026


Progress Tracker

Activity ID	Activity Name	Original Duration	Budgeted Total Cost	BL Project Start	BL Project Finish	Actual Start	Actual Finish	Planned Value Cost	Earned Value Cost	Schedule Performance Index
35 Meters mono pole with Double Platform for Access Points		285	32,000.00	13-Jan-26	06-Mar-27	30-Mar-26	04-May-26	0.00	32,000.00	0.00
CON-LEG101-PR-3800	PO for 35 Meters mono pole with Double Platform for Access Points	5	0.00	13-Jan-26	18-Jan-26	30-Mar-26	30-Mar-26	0.00	0.00	PO for 35 Meters mono pole with Double Platform for Access Points
CON-LEG101-PR-3810	Material Fabrication for 35 Meters mono pole with Double Platform for	90	0.00	30-Sep-26	12-Jan-27	04-Apr-26	30-Apr-26	0.00	0.00	0.00
CON-LEG101-PR-3820	Material Delivery for 35 Meters mono pole with Double Platform for Ac	20	32,000.00	13-Jan-27	04-Feb-27	02-May-26	04-May-26	0.00	32,000.00	0.00
CON-LEG101-PR-3830	Staging Time for 35 Meters mono pole with Double Platform for Access	20	0.00	06-Feb-27	06-Mar-27	02-May-26	04-May-26	0.00	0.00	0.00
25 Meters pole for CCTV Cameras		218	156,000.00	13-Jan-26	30-Nov-26	30-Mar-26	04-May-26	10,400.00	156,000.00	15.00
CON-LEG101-PR-3840	PO for 25 Meters pole for CCTV Cameras	5	0.00	13-Jan-26	18-Jan-26	30-Mar-26	30-Mar-26	0.00	0.00	0.00
CON-LEG101-PR-3850	Material Fabrication for 25 Meters pole for CCTV Cameras	90	0.00	13-Jul-26	26-Oct-26	04-Apr-26	30-Apr-26	0.00	0.00	0.00
CON-LEG101-PR-3860	Material Delivery for 25 Meters pole for CCTV Cameras	15	156,000.00	27-Oct-26	12-Nov-26	02-May-26	04-May-26	10,400.00	156,000.00	15.00
CON-LEG101-PR-3870	Staging Time for 25 Meters pole for CCTV Cameras	15	0.00	14-Nov-26	30-Nov-26	02-May-26	04-May-26	0.00	0.00	0.00
Short Range wireless point to point wireless bridge		221	31,200.00	13-Jan-26	24-Nov-26	30-Mar-26	04-May-26	2,080.00	31,200.00	15.00
CON-LEG101-PR-3880	PO for Short Range wireless point to point wireless bridge	5	0.00	13-Jan-26	18-Jan-26	30-Mar-26	30-Mar-26	0.00	0.00	0.00
CON-LEG101-PR-3890	Material Fabrication for Short Range wireless point to point wireless bri	90	0.00	13-Jul-26	26-Oct-26	04-Apr-26	30-Apr-26	0.00	0.00	0.00
CON-LEG101-PR-3900	Material Delivery for Short Range wireless point to point wireless bri	15	31,200.00	27-Oct-26	12-Nov-26	02-May-26	04-May-26	2,080.00	31,200.00	15.00
CON-LEG101-PR-3910	Staging Time for Short Range wireless point to point wireless bridge	10	0.00	14-Nov-26	24-Nov-26	02-May-26	04-May-26	0.00	0.00	0.00
Landscape Works		424	392,390.00	10-Jan-26	14-Sep-27	01-Jan-26		0.00	191,860.00	0.00
HDPE Pipes		330	28,800.00	10-Jan-26	23-Dec-26	01-Jan-26	21-Feb-26	0.00	28,800.00	0.00
CON-LEG101-PR-3920	PO for HDPE Pipes	7	0.00	10-Jan-26	17-Jan-26	01-Jan-26	01-Jan-26	0.00	0.00	0.00
CON-LEG101-PR-3930	Material Fabrication for HDPE Pipes	60	0.00	06-Aug-26	15-Oct-26	03-Jan-26	09-Feb-26	0.00	0.00	0.00
CON-LEG101-PR-3940	Material Delivery for HDPE Pipes	15	28,800.00	25-Nov-26	12-Dec-26	10-Feb-26	21-Feb-26	0.00	28,800.00	0.00
CON-LEG101-PR-3980	Staging Time for HDPE Pipes	10	0.00	13-Dec-26	23-Dec-26	12-Feb-26	21-Feb-26	0.00	0.00	0.00
Curbs and edging		263	8,160.00	13-Jan-26	17-Jan-27	01-Feb-26	28-Jul-26	0.00	8,160.00	0.00
CON-LEG101-PR-2890	PO for Curbs and edging	5	0.00	13-Jan-26	18-Jan-26	01-Feb-26	02-Feb-26	0.00	0.00	0.00
CON-LEG101-PR-2950	Material Fabrication for Curbs and edging	60	0.00	17-Oct-26	24-Dec-26	11-Apr-26	25-Jul-26	0.00	0.00	0.00
CON-LEG101-PR-3010	Material Delivery for Curbs and edging	10	8,160.00	26-Dec-26	05-Jan-27	01-Jul-26	26-Jul-26	0.00	8,160.00	0.00
CON-LEG101-PR-3070	Staging Time for Curbs and edging	10	0.00	06-Jan-27	17-Jan-27	02-Jul-26	28-Jul-26	0.00	0.00	0.00
Electrical Solenoid Valve		253	11,000.00	13-Jan-26	28-Jan-27	25-Mar-26	13-Oct-26	0.00	11,000.00	0.00
CON-LEG101-PR-2840	PO for Electrical Solenoid Valve	5	0.00	13-Jan-26	18-Jan-26	25-Mar-26	25-Mar-26	0.00	0.00	0.00
CON-LEG101-PR-2900	Material Fabrication for Electrical Solenoid Valve	60	0.00	28-Oct-26	05-Jan-27	11-Apr-26	05-Oct-26	0.00	0.00	0.00
CON-LEG101-PR-2960	Material Delivery for Electrical Solenoid Valve	10	11,000.00	06-Jan-27	17-Jan-27	06-Oct-26	10-Oct-26	0.00	11,000.00	0.00
CON-LEG101-PR-3020	Staging Time for Electrical Solenoid Valve	10	0.00	18-Jan-27	28-Jan-27	11-Oct-26	13-Oct-26	0.00	0.00	0.00
Quick coupler valve		267	7,200.00	13-Jan-26	18-Feb-27	25-Mar-26	13-Oct-26	0.00	7,200.00	0.00
CON-LEG101-PR-2850	PO for Quick coupler valve	5	0.00	13-Jan-26	18-Jan-26	25-Mar-26	25-Mar-26	0.00	0.00	0.00
CON-LEG101-PR-2910	Material Fabrication for Quick coupler valve	60	0.00	28-Oct-26	05-Jan-27	11-Apr-26	05-Oct-26	0.00	0.00	0.00
CON-LEG101-PR-2970	Material Delivery for Quick coupler valve	7	7,200.00	30-Jan-27	06-Feb-27	06-Oct-26	10-Oct-26	0.00	7,200.00	0.00
CON-LEG101-PR-3030	Staging Time for Quick coupler valve	7	0.00	07-Feb-27	18-Feb-27	11-Oct-26	13-Oct-26	0.00	0.00	0.00
Flush valve		287	20,000.00	13-Jan-26	15-Mar-27	25-Mar-26	13-Oct-26	0.00	20,000.00	0.00
CON-LEG101-PR-3080	PO for Flush valve	5	0.00	13-Jan-26	18-Jan-26	25-Mar-26	25-Mar-26	0.00	0.00	0.00
CON-LEG101-PR-3090	Material Fabrication for Flush valve	60	0.00	28-Oct-26	05-Jan-27	11-Apr-26	05-Oct-26	0.00	0.00	0.00
CON-LEG101-PR-3100	Material Delivery for Flush valve	10	20,000.00	20-Feb-27	03-Mar-27	06-Oct-26	10-Oct-26	0.00	20,000.00	0.00
CON-LEG101-PR-3110	Staging Time for Flush valve	10	0.00	04-Mar-27	15-Mar-27	11-Oct-26	13-Oct-26	0.00	0.00	0.00
Irrigation controller		307	70,000.00	13-Jan-26	07-Apr-27	25-Mar-26	13-Oct-26	0.00	70,000.00	0.00
CON-LEG101-PR-2860	PO for Irrigation controller	5	0.00	13-Jan-26	18-Jan-26	25-Mar-26	25-Mar-26	0.00	0.00	0.00
CON-LEG101-PR-2920	Material Fabrication for Irrigation controller	60	0.00	28-Oct-26	05-Jan-27	11-Apr-26	05-Oct-26	0.00	0.00	0.00
CON-LEG101-PR-2980	Material Delivery for Irrigation controller	10	70,000.00	16-Mar-27	27-Mar-27	06-Oct-26	10-Oct-26	0.00	70,000.00	0.00
CON-LEG101-PR-3040	Staging Time for Irrigation controller	10	0.00	28-Mar-27	07-Apr-27	11-Oct-26	13-Oct-26	0.00	0.00	0.00
Decoder for valve		330	8,000.00	13-Jan-26	04-May-27	25-Mar-26	13-Oct-26	0.00	8,000.00	0.00
CON-LEG101-PR-3120	PO for Decoder for valve	5	0.00	13-Jan-26	18-Jan-26	25-Mar-26	25-Mar-26	0.00	0.00	0.00
CON-LEG101-PR-3130	Material Fabrication for Decoder for valve	60	0.00	28-Oct-26	05-Jan-27	11-Apr-26	05-Oct-26	0.00	0.00	0.00
CON-LEG101-PR-3140	Material Delivery for Decoder for valve	13	8,000.00	08-Apr-27	22-Apr-27	06-Oct-26	10-Oct-26	0.00	8,000.00	0.00
CON-LEG101-PR-3150	Staging Time for Decoder for valve	10	0.00	24-Apr-27	04-May-27	11-Oct-26	13-Oct-26	0.00	0.00	0.00
Decoder Cables		340	38,700.00	13-Jan-26	20-May-27	25-Mar-26	13-Oct-26	0.00	38,700.00	0.00
CON-LEG101-PR-2870	PO for Decoder Cables	5	0.00	13-Jan-26	18-Jan-26	25-Mar-26	25-Mar-26	0.00	0.00	0.00

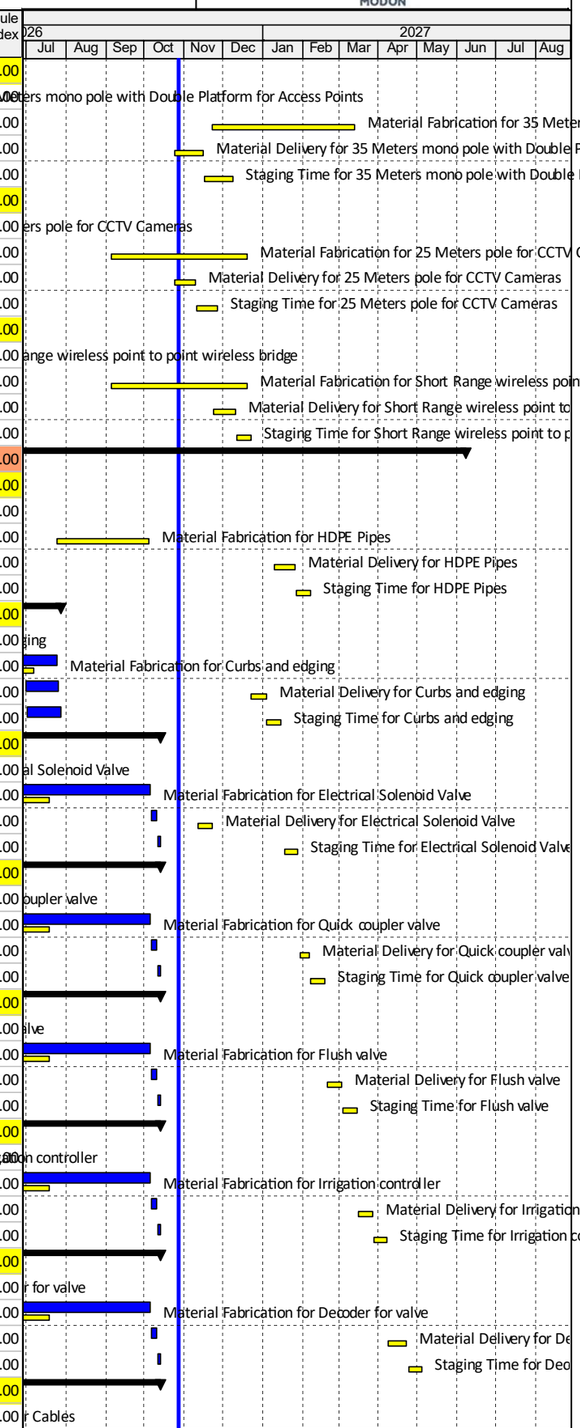


© Oracle Corporation

Activity ID	Activity Name	Original Duration	Budgeted Total Cost	BL Project Start	BL Project Finish	Actual Start	Actual Finish	Planned Value Cost	Earned Value Cost	Schedule Performance Index
CON-LEG101-PR-2930	Material Fabrication for Decoder Cables	60	0.00	28-Oct-26	05-Jan-27	11-Apr-26	05-Oct-26	0.00	0.00	0.00
CON-LEG101-PR-2990	Material Delivery for Decoder Cables	10	38,700.00	06-Jan-27	17-Jan-27	06-Oct-26	10-Oct-26	0.00	38,700.00	0.00
CON-LEG101-PR-3050	Staging Time for Decoder Cables	10	0.00	05-May-27	20-May-27	11-Oct-26	13-Oct-26	0.00	0.00	0.00
Shrubs And Ground Cover		351	200,530.00	13-Jan-26	14-Sep-27	25-Mar-26		0.00	0.00	0.00
CON-LEG101-PR-2880	PO for agricultural soil	5	0.00	13-Jan-26	18-Jan-26	25-Mar-26	25-Mar-26	0.00	0.00	0.00
CON-LEG101-PR-3000	Material Delivery for agricultural soil	90	200,530.00	22-May-27	02-Sep-27			0.00	0.00	0.00
CON-LEG101-PR-3060	Staging Time for agricultural soil	10	0.00	04-Sep-27	14-Sep-27			0.00	0.00	0.00
Bridge Works		367	340,315.00	06-Jan-26	19-May-27	01-Feb-26		181,600.00	257,915.00	1.42
Prestressing Strands		119	155,200.00	06-Jan-26	01-Jun-26	11-Feb-26	26-Mar-26	155,200.00	155,200.00	1.00
CON-LEG101-PR-2120	PO for Prestressing Strands	7	0.00	06-Jan-26	13-Jan-26	11-Feb-26	12-Feb-26	0.00	0.00	0.00
CON-LEG101-PR-2130	Material for Prestressing Strands	75	0.00	14-Jan-26	16-Apr-26	12-Feb-26	17-Mar-26	0.00	0.00	0.00
CON-LEG101-PR-2140	Material Delivery for Prestressing Strands	15	155,200.00	18-Apr-26	04-May-26	10-Mar-26	25-Mar-26	155,200.00	155,200.00	1.00
CON-LEG101-PR-2400	Staging Time for Prestressing Strands	20	0.00	05-May-26	01-Jun-26	11-Mar-26	26-Mar-26	0.00	0.00	0.00
Bridge Bearings		87	12,000.00	12-Jan-26	12-Jul-26	11-Feb-26	21-Apr-26	12,000.00	12,000.00	1.00
CON-LEG101-PR-2180	PO for Bridge Bearings	5	0.00	12-Jan-26	17-Jan-26	11-Feb-26	12-Feb-26	0.00	0.00	0.00
CON-LEG101-PR-2190	Material Fabrication for Bridge Bearings	75	0.00	18-Jan-26	20-Apr-26	12-Feb-26	02-Apr-26	0.00	0.00	0.00
CON-LEG101-PR-2200	Material Delivery for Bridge Bearings	15	12,000.00	02-Jun-26	18-Jun-26	19-Apr-26	20-Apr-26	12,000.00	12,000.00	1.00
CON-LEG101-PR-2240	Staging Time for Bridge Bearings	20	0.00	20-Jun-26	12-Jul-26	21-Apr-26	21-Apr-26	0.00	0.00	0.00
Bridge Gully (Scupper) drainage		142	4,800.00	12-Jan-26	27-Aug-26	25-Mar-26	21-Jun-26	4,800.00	4,800.00	1.00
CON-LEG101-PR-2370	PO for Bridge Gully (Scupper) drainage	5	0.00	12-Jan-26	17-Jan-26	25-Mar-26	25-Mar-26	0.00	0.00	0.00
CON-LEG101-PR-2380	Material Fabrication for Bridge Gully (Scupper) drainage	60	0.00	21-Apr-26	04-Jul-26	28-Mar-26	18-Jun-26	0.00	0.00	0.00
CON-LEG101-PR-2390	Material Delivery for Bridge Gully (Scupper) drainage	20	4,800.00	13-Jul-26	04-Aug-26	20-Jun-26	20-Jun-26	4,800.00	4,800.00	1.00
CON-LEG101-PR-2410	Staging Time for Bridge Gully (Scupper) drainage	20	0.00	05-Aug-26	27-Aug-26	21-Jun-26	21-Jun-26	0.00	0.00	0.00
New Jersey		182	9,600.00	12-Jan-26	06-Oct-26	01-Feb-26	21-Jun-26	9,600.00	9,600.00	1.00
CON-LEG101-PR-2150	PO for New Jersey	5	0.00	12-Jan-26	17-Jan-26	01-Feb-26	01-Feb-26	0.00	0.00	0.00
CON-LEG101-PR-2160	Material Fabrication for New Jersey	60	0.00	05-Jul-26	12-Sep-26	26-Mar-26	18-Jun-26	0.00	0.00	0.00
CON-LEG101-PR-2170	Material Delivery for New Jersey	10	9,600.00	13-Sep-26	24-Sep-26	20-Jun-26	20-Jun-26	9,600.00	9,600.00	1.00
CON-LEG101-PR-2420	Staging Time for New Jersey	10	0.00	26-Sep-26	06-Oct-26	21-Jun-26	21-Jun-26	0.00	0.00	0.00
Expansion Joints		281	22,715.00	12-Jan-26	07-Jan-27	11-Feb-26	21-Jun-26	0.00	22,715.00	0.00
CON-LEG101-PR-2210	PO for Expansion Joints	5	0.00	12-Jan-26	17-Jan-26	11-Feb-26	12-Feb-26	0.00	0.00	0.00
CON-LEG101-PR-2220	Material Fabrication for Expansion Joints	60	0.00	07-Oct-26	15-Dec-26	12-Feb-26	18-Jun-26	0.00	0.00	0.00
CON-LEG101-PR-2230	Material Delivery for Expansion Joints	10	22,715.00	16-Dec-26	27-Dec-26	20-Jun-26	20-Jun-26	0.00	22,715.00	0.00
CON-LEG101-PR-2250	Staging Time for Expansion Joints	10	0.00	28-Dec-26	07-Jan-27	21-Jun-26	21-Jun-26	0.00	0.00	0.00
Guard Rail		275	28,800.00	12-Jan-26	27-Mar-27	26-Mar-26		0.00	21,600.00	0.00
CON-LEG101-PR-2260	PO for Guard Rail	5	0.00	12-Jan-26	17-Jan-26	26-Mar-26	26-Mar-26	0.00	0.00	0.00
CON-LEG101-PR-2270	Material Fabrication for Guard Rail	75	0.00	07-Oct-26	02-Jan-27	28-Mar-26	15-Oct-26	0.00	0.00	0.00
CON-LEG101-PR-2280	Material Delivery for Guard Rail	15	28,800.00	09-Jan-27	25-Jan-27	17-Oct-26		0.00	21,600.00	0.00
CON-LEG101-PR-2290	Staging Time for Guard Rail	20	0.00	04-Mar-27	27-Mar-27			0.00	0.00	0.00
Logo MODON		328	32,000.00	12-Jan-26	19-May-27	26-Mar-26	30-Sep-26	0.00	32,000.00	0.00
CON-LEG101-PR-2340	PO for Logo MODON	5	0.00	12-Jan-26	17-Jan-26	26-Mar-26	26-Mar-26	0.00	0.00	0.00
CON-LEG101-PR-2350	Material Fabrication for Logo MODON	75	0.00	09-Jan-27	11-Apr-27	28-Mar-26	24-Sep-26	0.00	0.00	0.00
CON-LEG101-PR-2360	Material Delivery for Logo MODON	19	32,000.00	12-Apr-27	03-May-27	26-Sep-26	28-Sep-26	0.00	32,000.00	0.00
CON-LEG101-PR-2430	Staging Time for Logo MODON	10	0.00	04-May-27	19-May-27	30-Sep-26	30-Sep-26	0.00	0.00	0.00
GRP Panel		313	75,200.00	12-Jan-26	25-Apr-27	26-Mar-26		0.00	0.00	0.00
CON-LEG101-PR-2300	PO for GRP Panel	5	0.00	12-Jan-26	17-Jan-26	26-Mar-26	26-Mar-26	0.00	0.00	0.00
CON-LEG101-PR-2310	Material Fabrication for GRP Panel	60	0.00	09-Jan-27	24-Mar-27	28-Mar-26		0.00	0.00	0.00
CON-LEG101-PR-2320	Material Delivery for GRP Panel	15	75,200.00	28-Mar-27	13-Apr-27			0.00	0.00	0.00
CON-LEG101-PR-2330	Staging Time for GRP Panel	10	0.00	14-Apr-27	25-Apr-27			0.00	0.00	0.00
Irrigation Works		422	218,760.00	12-Jan-26	28-Jun-27	25-Mar-26	11-Oct-26	0.00	218,760.00	0.00
Flush valve		422	0.00	17-Jan-26	08-May-27	25-Mar-26	11-Oct-26	0.00	0.00	0.00
CON-LEG101-PR-2640	PO for Flush valve	3	0.00	17-Jan-26	19-Jan-26	25-Mar-26	25-Mar-26	0.00	0.00	0.00
CON-LEG101-PR-2680	Material Fabrication for Flush valve	60	0.00	18-Jan-27	03-Apr-27	11-Apr-26	05-Oct-26	0.00	0.00	0.00
CON-LEG101-PR-2720	Material Delivery for Flush valve	20	0.00	04-Apr-27	26-Apr-27	06-Oct-26	08-Oct-26	0.00	0.00	0.00

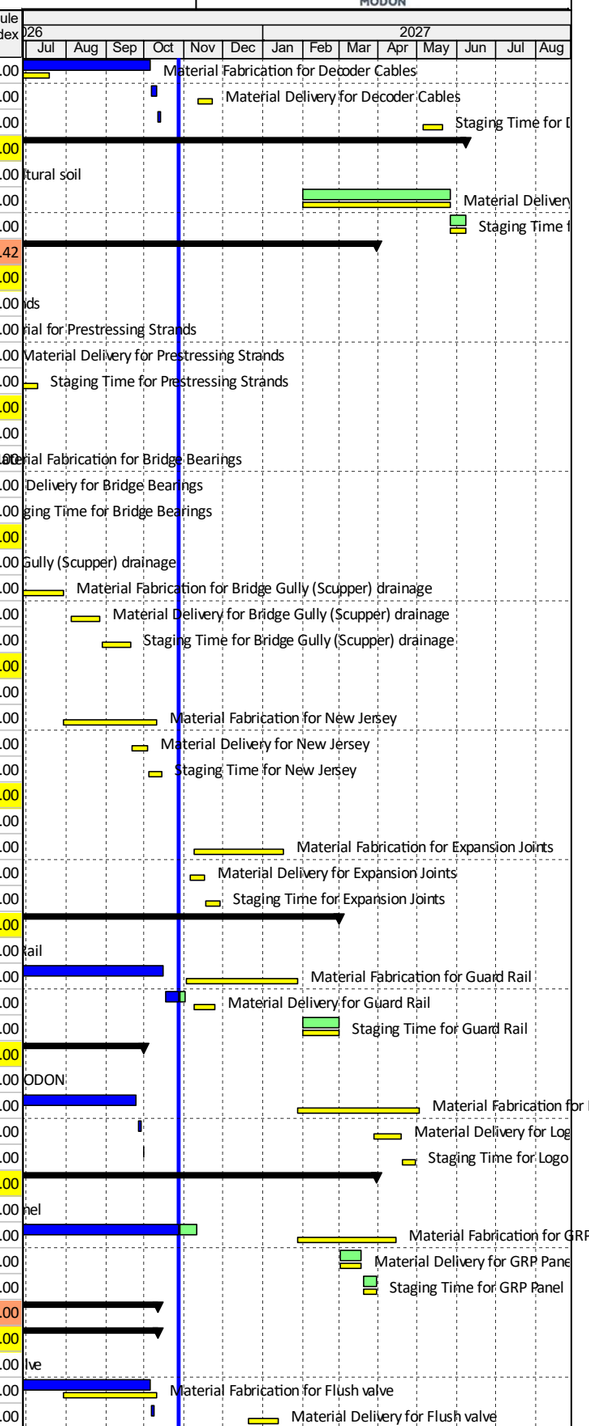


© Oracle Corporation

Activity ID	Activity Name	Original Duration	Budgeted Total Cost	BL Project Start	BL Project Finish	Actual Start	Actual Finish	Planned Value Cost	Earned Value Cost	Schedule Performance Index
CON-LEG101-PR-2760	Staging Time for Flush valve	10	0.00	27-Apr-27	08-May-27	10-Oct-26	11-Oct-26	0.00	0.00	0.00
16 mm dia (O.D.) linear low density polyethylene tubing		167	218,760.00	12-Jan-26	11-May-27	25-Mar-26	20-Apr-26	0.00	218,760.00	0.00
CON-LEG101-PR-2650	PO for 16 mm dia (O.D.) linear low density polyethylene tubing	7	0.00	12-Jan-26	19-Jan-26	25-Mar-26	25-Mar-26	0.00	0.00	0.00
CON-LEG101-PR-2690	Material Fabrication for 16 mm dia (O.D.) linear low density polyethyle	70	0.00	18-Jan-27	14-Apr-27	11-Apr-26	16-Apr-26	0.00	0.00	0.00
CON-LEG101-PR-2730	Material Delivery for 16 mm dia (O.D.) linear low density polyethyler	13	218,760.00	15-Apr-27	29-Apr-27	18-Apr-26	19-Apr-26	0.00	218,760.00	0.00
CON-LEG101-PR-2770	Staging Time for 16 mm dia (O.D.) linear low density polyethylene tu	10	0.00	01-May-27	11-May-27	20-Apr-26	20-Apr-26	0.00	0.00	0.00
Irrigation Controller		368	0.00	14-Jan-26	20-Jun-27	25-Mar-26	20-Apr-26	0.00	0.00	0.00
CON-LEG101-PR-2660	PO for Irrigation Controller	5	0.00	14-Jan-26	19-Jan-26	25-Mar-26	25-Mar-26	0.00	0.00	PO for Irrigation Controller 0.00
CON-LEG101-PR-2700	Material Fabrication for Irrigation Controller	75	0.00	26-Jan-27	28-Apr-27	11-Apr-26	16-Apr-26	0.00	0.00	0.00
CON-LEG101-PR-2740	Material Delivery for Irrigation Controller	20	0.00	12-May-27	08-Jun-27	18-Apr-26	19-Apr-26	0.00	0.00	0.00
CON-LEG101-PR-2780	Staging Time for Irrigation Controller	10	0.00	09-Jun-27	20-Jun-27	20-Apr-26	20-Apr-26	0.00	0.00	0.00
Single station decoder		185	0.00	15-Jan-26	14-Jun-27	25-Mar-26	20-Apr-26	0.00	0.00	0.00
CON-LEG101-PR-2800	PO for Single station decoder	4	0.00	15-Jan-26	19-Jan-26	25-Mar-26	25-Mar-26	0.00	0.00	PO for Single station decoder 0.00
CON-LEG101-PR-2810	Material Fabrication for Single station decoder	75	0.00	02-Feb-27	05-May-27	11-Apr-26	16-Apr-26	0.00	0.00	0.00
CON-LEG101-PR-2820	Material Delivery for Single station decoder	20	0.00	06-May-27	02-Jun-27	18-Apr-26	19-Apr-26	0.00	0.00	0.00
CON-LEG101-PR-2830	Staging Time for Single station decoder	10	0.00	03-Jun-27	14-Jun-27	20-Apr-26	20-Apr-26	0.00	0.00	0.00
Decoder cables 12 AWG		192	0.00	17-Jan-26	28-Jun-27	25-Mar-26	20-Apr-26	0.00	0.00	0.00
CON-LEG101-PR-2670	PO for Decoder cables 12 AWG	3	0.00	17-Jan-26	19-Jan-26	25-Mar-26	25-Mar-26	0.00	0.00	0.00
CON-LEG101-PR-2710	Material Fabrication for Decoder cables 12 AWG	75	0.00	15-Feb-27	13-May-27	11-Apr-26	16-Apr-26	0.00	0.00	0.00
CON-LEG101-PR-2750	Material Delivery for Decoder cables 12 AWG	20	0.00	19-May-27	10-Jun-27	18-Apr-26	19-Apr-26	0.00	0.00	0.00
CON-LEG101-PR-2790	Staging Time for Decoder cables 12 AWG	15	0.00	12-Jun-27	28-Jun-27	20-Apr-26	20-Apr-26	0.00	0.00	0.00
Construction		716	58,147,531.04	20-Dec-25	18-Oct-27	20-Nov-25		30,381,826.03	45,367,535.69	1.49
Site Demolition		93	279,942.75	20-Dec-25	03-Mar-26	20-Nov-25	02-Feb-26	279,942.75	279,942.75	1.00
CON-LEG101-SD-1000	Removal of chain link fence [Demolition Works]	21	50,534.75	20-Dec-25	12-Jan-26	20-Nov-25	30-Nov-25	50,534.75	50,534.75	Removal of chain link fence [Demolition Works] 1.00
CON-LEG101-SD-1010	Removal of concrete fence [Demolition Works]	21	108,808.00	13-Jan-26	05-Feb-26	24-Nov-25	03-Dec-25	108,808.00	108,808.00	Removal of concrete fence [Demolition Works] 1.00
CON-LEG101-SD-1030	Demolition of existing structures [Demolition Works]	21	117,250.00	13-Jan-26	05-Feb-26	20-Nov-25	04-Dec-25	117,250.00	117,250.00	Demolition of existing structures [Demolition Works] 1.00
CON-LEG101-SD-1020	Removal of Electricity distribution panel [Demolition Works]	21	3,350.00	07-Feb-26	03-Mar-26	01-Feb-26	02-Feb-26	3,350.00	3,350.00	Removal of Electricity distribution panel [Demolition Works] 1.00
Roads & Meduim Voltage		429	11,810,038.74	06-Jan-26	17-Sep-26	01-Dec-25		11,810,038.74	8,650,438.79	0.73
Local – 01		415	5,046,733.52	06-Jan-26	17-Sep-26	01-Dec-25		5,046,733.52	3,821,245.32	0.76
LOCAL - 01 Segment-01 (From 0+000 to 1+066)		377	1,668,845.14	06-Jan-26	17-Aug-26	01-Dec-25		1,668,845.14	1,273,748.94	0.76
Road Works		194	1,253,220.74	20-Jan-26	17-Aug-26	01-Dec-25	16-Jul-26	1,253,220.74	1,253,220.74	1.00
Earthworks and Site Grading		91	500,060.34	20-Jan-26	11-May-26	01-Dec-25	20-Apr-26	500,060.34	500,060.34	1.00
CON-LEG101-LR-4570	Embankments to the parcels for roads [Local – 01 Segment-01]	21	190,236.60	18-Apr-26	11-May-26	06-Dec-25	29-Dec-25	190,236.60	190,236.60	Embankments to the parcels for roads [Local – 01 Segment-01] 1.00
CON-LEG101-LR-1360	Excavation for Roadway [Local – 01 Segment-01]	21	25,617.86	20-Jan-26	12-Feb-26	15-Dec-25	19-Apr-26	25,617.86	25,617.86	Excavation for Roadway [Local – 01 Segment-01] 1.00
CON-LEG101-LR-2760	Parcrels Excavation for Roadway [Local – 01 Segment-01]	20	16,556.38	14-Feb-26	09-Mar-26	01-Dec-25	19-Apr-26	16,556.38	16,556.38	Parcrels Excavation for Roadway [Local – 01 Segment-01] 1.00
CON-LEG101-LR-4070	Embankments to the roads [Local – 01 Segment-01]	15	267,649.50	10-Mar-26	31-Mar-26	17-Dec-25	20-Apr-26	267,649.50	267,649.50	Embankments to the roads [Local – 01 Segment-01] 1.00
Asphalt Work		67	753,160.40	16-Jun-26	17-Aug-26	25-Dec-25	16-Jul-26	753,160.40	753,160.40	1.00
CON-LEG101-LR-5580	Subgrade [Local – 01 Segment-01]	14	119,972.80	16-Jun-26	01-Jul-26	25-Dec-25	27-Apr-26	119,972.80	119,972.80	Subgrade [Local – 01 Segment-01] 1.00
CON-LEG101-LR-5680	Aggregate base course [Local – 01 Segment-01]	10	149,966.40	23-Jul-26	03-Aug-26	28-Apr-26	14-Jul-26	149,966.40	149,966.40	Aggregate base course [Local – 01 Segment-01] 1.00
CON-LEG101-LR-5780	Prime Coat (MC1) [Local – 01 Segment-01]	6	144,965.20	04-Aug-26	10-Aug-26	14-May-26	15-Jul-26	144,965.20	144,965.20	Prime Coat (MC1) [Local – 01 Segment-01] 1.00
CON-LEG101-LR-5880	Bituminous Base Course [Local – 01 Segment-01]	6	338,256.00	11-Aug-26	17-Aug-26	19-May-26	16-Jul-26	338,256.00	338,256.00	Bituminous Base Course [Local – 01 Segment-01] 1.00
Electrical Works		185	415,624.40	06-Jan-26	16-Jul-26	11-Apr-26		415,624.40	20,528.20	0.05
CON-LEG101-LR-15000	Approval of Subcontractor / Supplier / Consultant for Medium Voltag	10	0.00	06-Jan-26	17-Jan-26			0.00	0.00	0.00
CON-LEG101-LR-15010	Approval Materials of Medium Voltage from SEC	10	0.00	18-Jan-26	28-Jan-26			0.00	0.00	0.00
CON-LEG101-LR-15020	Testing Materials of Medium Voltage from SEC	5	0.00	18-Apr-26	22-Apr-26			0.00	0.00	0.00
CON-LEG101-LR-15030	PO for Medium Voltage	2	0.00	29-Jan-26	31-Jan-26			0.00	0.00	0.00
Medium Voltage		185	415,624.40	02-Jun-26	16-Jul-26	11-Apr-26		415,624.40	20,528.20	0.05
CON-LEG101-LR-6970	Installation of Medium Voltage Cables Duct Banks [Local – 01 Segment	10	20,528.20	10-Jun-26	21-Jun-26	11-Apr-26	30-Apr-26	20,528.20	20,528.20	1.00
CON-LEG101-LR-6880	Excavation for Medium Voltage trench [Local – 01 Segment-01]	7	16,297.20	02-Jun-26	09-Jun-26			16,297.20	0.00	0.00
CON-LEG101-LR-7060	Installation of Medium Voltage Cables [Local – 01 Segment-01]	7	320,595.00	22-Jun-26	29-Jun-26			320,595.00	0.00	0.00
CON-LEG101-LR-7150	Installation of Straight joints cables [Local – 01 Segment-01]	2	10,136.00	30-Jun-26	01-Jul-26			10,136.00	0.00	0.00
CON-LEG101-LR-7240	Installation of Cable Termination for 13.8 kv 3Cx 500 mm², Al /XLPE/LL	3	7,868.00	02-Jul-26	05-Jul-26			7,868.00	0.00	0.00
CON-LEG101-LR-7330	Installation of Medium Voltage Switchgears [Local – 01 Segment-01]	7	40,200.00	06-Jul-26	13-Jul-26			40,200.00	0.00	0.00

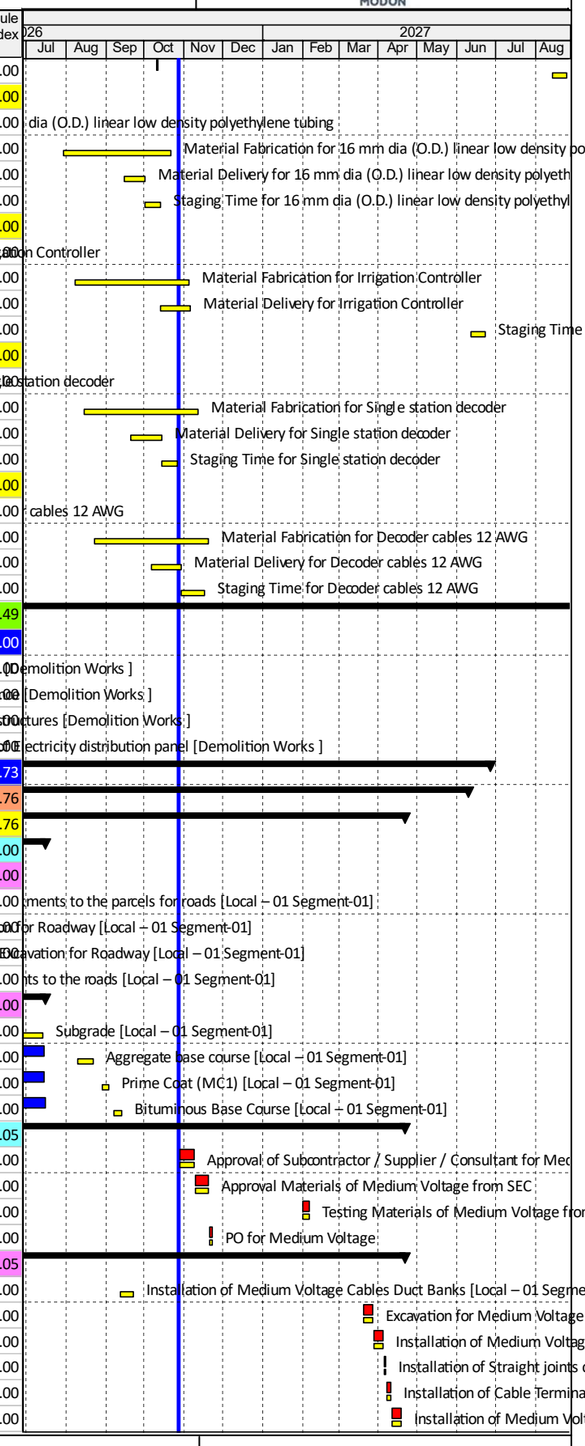


© Oracle Corporation

Activity ID	Activity Name	Original Duration	Budgeted Total Cost	BL Project Start	BL Project Finish	Actual Start	Actual Finish	Planned Value Cost	Earned Value Cost	Schedule Performance Index
CON-LEG101-LR-7680	Installation of Cable Termination [Local – 01 Segment-01]	3	0.00	14-Jul-26	16-Jul-26			0.00	0.00	0.00
LOCAL - 01 Segment-02 (From 1+066 to 2+133)		377	1,668,843.64	20-Jan-26	31-Aug-26	06-Dec-25		1,668,843.64	1,273,747.44	0.76
Road Works		240	1,253,219.24	20-Jan-26	31-Aug-26	06-Dec-25	14-Jun-26	1,253,219.24	1,253,219.24	1.00
Earthworks and Site Grading		63	500,058.84	20-Jan-26	26-Apr-26	06-Dec-25	15-Apr-26	500,058.84	500,058.84	1.00
CON-LEG101-LR-2770	Parcrels Excavation for Roadway [Local – 01 Segment-02]	18	16,556.38	14-Feb-26	07-Mar-26	06-Dec-25	11-Dec-25	16,556.38	16,556.38	1.00
CON-LEG101-LR-1450	Excavation for Roadway [Local – 01 Segment-02]	21	25,617.86	20-Jan-26	12-Feb-26	16-Dec-25	19-Jan-26	25,617.86	25,617.86	1.00
CON-LEG101-LR-4170	Embankments to the roads [Local – 01 Segment-02]	19	267,649.50	08-Mar-26	02-Apr-26	17-Dec-25	20-Jan-26	267,649.50	267,649.50	1.00
CON-LEG101-LR-4640	Embankments to the parcels for roads [Local – 01 Segment-02]	20	190,235.10	04-Apr-26	26-Apr-26	13-Dec-25	15-Apr-26	190,235.10	190,235.10	1.00
Asphalt Work		138	753,160.40	17-Jun-26	31-Aug-26	29-Dec-25	14-Jun-26	753,160.40	753,160.40	1.00
CON-LEG101-LR-5590	Subgrade [Local – 01 Segment-02]	14	119,972.80	17-Jun-26	02-Jul-26	29-Dec-25	02-May-26	119,972.80	119,972.80	1.00
CON-LEG101-LR-5690	Aggregate base course [Local – 01 Segment-02]	14	149,966.40	02-Aug-26	17-Aug-26	03-May-26	21-May-26	149,966.40	149,966.40	1.00
CON-LEG101-LR-5790	Prime Coat (MC1) [Local – 01 Segment-02]	6	144,965.20	18-Aug-26	24-Aug-26	18-May-26	06-Jun-26	144,965.20	144,965.20	1.00
CON-LEG101-LR-5890	Bituminous Base Course [Local – 01 Segment-02]	6	338,256.00	25-Aug-26	31-Aug-26	20-May-26	14-Jun-26	338,256.00	338,256.00	1.00
Electrical Works		193	415,624.40	15-Jun-26	04-Aug-26	14-Apr-26		415,624.40	20,528.20	0.05
Medium Voltage		193	415,624.40	15-Jun-26	04-Aug-26	14-Apr-26		415,624.40	20,528.20	0.05
CON-LEG101-LR-6980	Installation of Medium Voltage Cables Duct Banks [Local – 01 Segment	10	20,528.20	23-Jun-26	04-Jul-26	14-Apr-26	30-Apr-26	20,528.20	20,528.20	1.00
CON-LEG101-LR-6890	Excavation for Medium Voltage trench [Local – 01 Segment-02]	7	16,297.20	15-Jun-26	22-Jun-26			16,297.20	0.00	0.00
CON-LEG101-LR-7070	Installation of Medium Voltage Cables [Local – 01 Segment-02]	7	320,595.00	05-Jul-26	12-Jul-26			320,595.00	0.00	0.00
CON-LEG101-LR-7160	Installation of Straight joints cables [Local – 01 Segment-02]	5	10,136.00	13-Jul-26	18-Jul-26			10,136.00	0.00	0.00
CON-LEG101-LR-7250	Installation of Cable Termination for 13.8 kv 3Cx 500 mm², Al /XLPE/LLI	3	7,868.00	19-Jul-26	21-Jul-26			7,868.00	0.00	0.00
CON-LEG101-LR-7340	Installation of Medium Voltage Switchgears [Local – 01 Segment-02]	7	40,200.00	22-Jul-26	29-Jul-26			40,200.00	0.00	0.00
CON-LEG101-LR-7690	Installation of Cable Termination [Local – 01 Segment-02]	5	0.00	30-Jul-26	04-Aug-26			0.00	0.00	0.00
LOCAL - 01 Segment-03 (From 2+133 to 3+200)		367	1,709,044.74	10-Mar-26	17-Sep-26	28-Dec-25		1,709,044.74	1,273,748.94	0.75
Road Works		277	1,253,220.74	10-Mar-26	09-Sep-26	28-Dec-25	10-Sep-26	1,253,220.74	1,253,220.74	1.00
Earthworks and Site Grading		86	500,060.34	10-Mar-26	21-Jun-26	28-Dec-25	10-Sep-26	500,060.34	500,060.34	1.00
CON-LEG101-LR-1540	Excavation for Roadway [Local – 01 Segment-03]	21	25,617.86	10-Mar-26	07-Apr-26	28-Mar-26	05-Jul-26	25,617.86	25,617.86	1.00
CON-LEG101-LR-4270	Embankments to the roads [Local – 01 Segment-03]	21	267,649.50	29-Apr-26	23-May-26	30-Mar-26	05-Jul-26	267,649.50	267,649.50	1.00
CON-LEG101-LR-4710	Embankments to the parcels for roads [Local – 01 Segment-03]	21	190,236.60	24-May-26	21-Jun-26	28-Dec-25	08-Jul-26	190,236.60	190,236.60	1.00
CON-LEG101-LR-2860	Parcrels Excavation for Roadway [Local – 01 Segment-03]	18	16,556.38	08-Apr-26	28-Apr-26	28-Dec-25	10-Sep-26	16,556.38	16,556.38	1.00
Asphalt Work		122	753,160.40	15-Jul-26	09-Sep-26	17-Jun-26	26-Jul-26	753,160.40	753,160.40	1.00
CON-LEG101-LR-5600	Subgrade [Local – 01 Segment-03]	14	119,972.80	15-Jul-26	30-Jul-26	17-Jun-26	13-Jul-26	119,972.80	119,972.80	1.00
CON-LEG101-LR-5700	Aggregate base course [Local – 01 Segment-03]	10	149,966.40	05-Aug-26	16-Aug-26	11-Jul-26	23-Jul-26	149,966.40	149,966.40	1.00
CON-LEG101-LR-5800	Prime Coat (MC1) [Local – 01 Segment-03]	8	144,965.20	17-Aug-26	25-Aug-26	18-Jul-26	25-Jul-26	144,965.20	144,965.20	1.00
CON-LEG101-LR-5900	Bituminous Base Course [Local – 01 Segment-03]	8	338,256.00	01-Sep-26	09-Sep-26	19-Jul-26	26-Jul-26	338,256.00	338,256.00	1.00
Electrical Works		121	455,824.00	17-Aug-26	17-Sep-26	20-Jun-26		455,824.00	20,528.20	0.05
Medium Voltage		121	455,824.00	17-Aug-26	17-Sep-26	20-Jun-26		455,824.00	20,528.20	0.05
CON-LEG101-LR-6990	Installation of Medium Voltage Cables Duct Banks [Local – 01 Segment	5	20,528.20	22-Aug-26	26-Aug-26	20-Jun-26	14-Jul-26	20,528.20	20,528.20	1.00
CON-LEG101-LR-6900	Excavation for Medium Voltage trench [Local – 01 Segment-03]	4	16,296.80	17-Aug-26	20-Aug-26			16,296.80	0.00	0.00
CON-LEG101-LR-7080	Installation of Medium Voltage Cables [Local – 01 Segment-03]	7	320,595.00	27-Aug-26	03-Sep-26			320,595.00	0.00	0.00
CON-LEG101-LR-7170	Installation of Straight joints cables [Local – 01 Segment-03]	2	10,136.00	05-Sep-26	06-Sep-26			10,136.00	0.00	0.00
CON-LEG101-LR-7260	Installation of Cable Termination for 13.8 kv 3Cx 500 mm², Al /XLPE/LLI	3	7,868.00	07-Sep-26	09-Sep-26			7,868.00	0.00	0.00
CON-LEG101-LR-7350	Installation of Medium Voltage Switchgears [Local – 01 Segment-03]	4	80,400.00	10-Sep-26	14-Sep-26			80,400.00	0.00	0.00
CON-LEG101-LR-7700	Installation of Cable Termination [Local – 01 Segment-03]	3	0.00	15-Sep-26	17-Sep-26			0.00	0.00	0.00
Local – 02		367	1,522,313.70	16-Mar-26	16-Sep-26	08-Dec-25		1,522,313.70	940,681.70	0.62
Road Works		267	911,944.80	16-Mar-26	16-Sep-26	08-Dec-25	21-Jun-26	911,944.80	911,944.80	1.00
Earthworks and Site Grading		137	409,824.32	16-Mar-26	22-Aug-26	08-Dec-25	18-Jun-26	409,824.32	409,824.32	1.00
CON-LEG101-LR-1630	Excavation for Roadway [Local – 02]	21	17,735.44	16-Mar-26	13-Apr-26	24-Dec-25	29-Dec-25	17,735.44	17,735.44	1.00
CON-LEG101-LR-4310	Embankments to the roads [Local – 02]	21	185,295.90	13-Jul-26	05-Aug-26	29-Dec-25	03-Jan-26	185,295.90	185,295.90	1.00
CON-LEG101-LR-2950	Parcrels Excavation for Roadway [Local – 02]	18	16,556.38	22-Jun-26	12-Jul-26	08-Dec-25	05-Jan-26	16,556.38	16,556.38	1.00
CON-LEG101-LR-4780	Embankments to the parcels for roads [Local – 02]	14	190,236.60	06-Aug-26	22-Aug-26	13-Dec-25	18-Jun-26	190,236.60	190,236.60	1.00
Asphalt Work		171	502,120.48	23-Aug-26	16-Sep-26	12-Jan-26	21-Jun-26	502,120.48	502,120.48	1.00
CON-LEG101-LR-5610	Subgrade [Local – 02]	7	79,982.08	23-Aug-26	30-Aug-26	12-Jan-26	25-Jan-26	79,982.08	79,982.08	1.00
CON-LEG101-LR-5710	Aggregate base course [Local – 02]	9	99,977.40	31-Aug-26	09-Sep-26	09-Jun-26	18-Jun-26	99,977.40	99,977.40	1.00

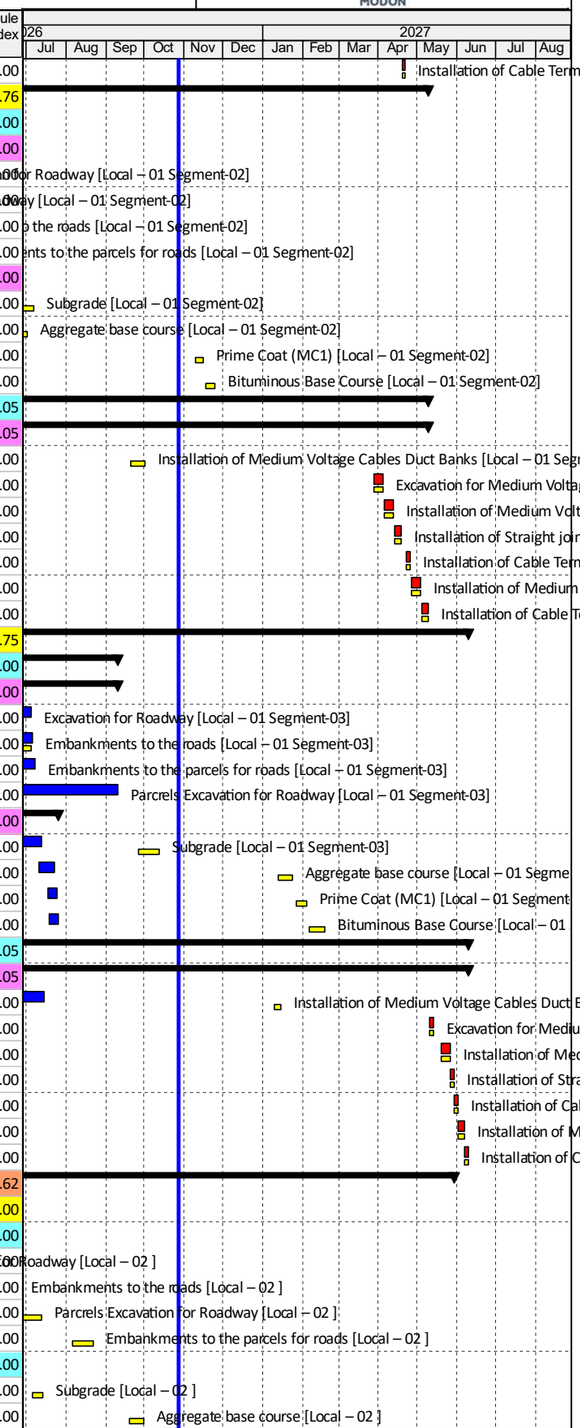


© Oracle Corporation

Activity ID	Activity Name	Original Duration	Budgeted Total Cost	BL Project Start	BL Project Finish	Actual Start	Actual Finish	Planned Value Cost	Earned Value Cost	Schedule Performance Index
CON-LEG101-LR-5810	Prime Coat (MC1) [Local – 02]	2	96,657.00	10-Sep-26	12-Sep-26	11-Jun-26	20-Jun-26	96,657.00	96,657.00	1.00
CON-LEG101-LR-5910	Bituminous Base Course [Local – 02]	4	225,504.00	13-Sep-26	16-Sep-26	15-Jun-26	21-Jun-26	225,504.00	225,504.00	1.00
Electrical Works		159	610,368.90	23-Jun-26	20-Aug-26	31-May-26		610,368.90	28,736.90	0.05
Medium Voltage		159	610,368.90	23-Jun-26	20-Aug-26	31-May-26		610,368.90	28,736.90	0.05
CON-LEG101-LR-7000	Installation of Medium Voltage Cables Duct Banks [Local – 02]	8	28,736.90	02-Jul-26	11-Jul-26	31-May-26	09-Jun-26	28,736.90	28,736.90	1.00
CON-LEG101-LR-6910	Excavation for Medium Voltage trench [Local – 02]	8	22,816.00	23-Jun-26	01-Jul-26			22,816.00	0.00	0.00
CON-LEG101-LR-7090	Installation of Medium Voltage Cables [Local – 02]	13	450,508.00	12-Jul-26	26-Jul-26			450,508.00	0.00	0.00
CON-LEG101-LR-7180	Installation of Straight joints cables [Local – 02]	6	14,196.00	27-Jul-26	02-Aug-26			14,196.00	0.00	0.00
CON-LEG101-LR-7270	Installation of Cable Termination for 13.8 kv 3Cx 500 mm², Al /XLPE/LLI	8	11,032.00	03-Aug-26	11-Aug-26			11,032.00	0.00	0.00
CON-LEG101-LR-7360	Installation of Medium Voltage Switchgears [Local – 02]	5	80,400.00	12-Aug-26	17-Aug-26			80,400.00	0.00	0.00
CON-LEG101-LR-7710	Installation of Cable Termination [Local – 02]	3	2,680.00	18-Aug-26	20-Aug-26			2,680.00	0.00	0.00
Local – 03		395	823,136.20	14-Apr-26	17-Sep-26	08-Dec-25		823,136.20	700,463.80	0.85
Road Works		290	693,622.50	14-Apr-26	17-Sep-26	08-Dec-25	10-Sep-26	693,622.50	693,622.50	1.00
Earthworks and Site Grading		155	342,147.30	14-Apr-26	02-Sep-26	08-Dec-25	10-Sep-26	342,147.30	342,147.30	1.00
CON-LEG101-LR-1740	Excavation for Roadway [Local – 03]	14	11,823.62	14-Apr-26	29-Apr-26	05-Jan-26	08-Jan-26	11,823.62	11,823.62	Excavation for Roadway [Local – 03]
CON-LEG101-LR-3040	Parcrels Excavation for Roadway [Local – 03]	14	16,556.38	13-Jul-26	28-Jul-26	08-Dec-25	30-Mar-26	16,556.38	16,556.38	1.00
CON-LEG101-LR-4360	Embankments to the roads [Local – 03]	15	123,530.70	29-Jul-26	15-Aug-26	06-Jan-26	31-Mar-26	123,530.70	123,530.70	1.00
CON-LEG101-LR-4820	Embankments to the parcels for roads [Local – 03]	16	190,236.60	16-Aug-26	02-Sep-26	13-Dec-25	10-Sep-26	190,236.60	190,236.60	1.00
Asphalt Work		183	351,475.20	03-Sep-26	17-Sep-26	29-Jan-26	04-Aug-26	351,475.20	351,475.20	1.00
CON-LEG101-LR-5620	Subgrade [Local – 03]	4	55,987.20	03-Sep-26	07-Sep-26	29-Jan-26	30-Apr-26	55,987.20	55,987.20	1.00
CON-LEG101-LR-5720	Aggregate base course [Local – 03]	4	69,984.00	08-Sep-26	12-Sep-26	28-Jul-26	30-Jul-26	69,984.00	69,984.00	1.00
CON-LEG101-LR-5820	Prime Coat (MC1) [Local – 03]	2	67,651.20	13-Sep-26	14-Sep-26	02-Aug-26	02-Aug-26	67,651.20	67,651.20	1.00
CON-LEG101-LR-5920	Bituminous Base Course [Local – 03]	3	157,852.80	15-Sep-26	17-Sep-26	03-Aug-26	04-Aug-26	157,852.80	157,852.80	1.00
Electrical Works		163	129,513.70	22-Aug-26	17-Sep-26	21-Apr-26		129,513.70	6,841.30	0.05
Medium Voltage		163	129,513.70	22-Aug-26	17-Sep-26	21-Apr-26		129,513.70	6,841.30	0.05
CON-LEG101-LR-7010	Installation of Medium Voltage Cables Duct Banks [Local – 03]	4	6,841.30	25-Aug-26	29-Aug-26	21-Apr-26	07-May-26	6,841.30	6,841.30	1.00
CON-LEG101-LR-6920	Excavation for Medium Voltage trench [Local – 03]	3	5,432.40	22-Aug-26	24-Aug-26			5,432.40	0.00	0.00
CON-LEG101-LR-7100	Installation of Medium Voltage Cables [Local – 03]	5	108,540.00	30-Aug-26	03-Sep-26			108,540.00	0.00	0.00
CON-LEG101-LR-7190	Installation of Straight joints cables [Local – 03]	2	3,388.00	05-Sep-26	06-Sep-26			3,388.00	0.00	0.00
CON-LEG101-LR-7280	Installation of Cable Termination for 13.8 kv 3Cx 500 mm², Al /XLPE/LLI	3	2,632.00	07-Sep-26	09-Sep-26			2,632.00	0.00	0.00
CON-LEG101-LR-7370	Installation of Medium Voltage Switchgears [Local – 03]	4	0.00	10-Sep-26	14-Sep-26			0.00	0.00	0.00
CON-LEG101-LR-7720	Installation of Cable Termination [Local – 03]	3	2,680.00	15-Sep-26	17-Sep-26			2,680.00	0.00	0.00
Local – 04		333	808,919.60	30-Apr-26	17-Sep-26	10-Dec-25		808,919.60	206,792.98	0.26
Road Works		211	693,622.50	30-Apr-26	17-Sep-26	10-Dec-25		693,622.50	206,792.98	0.30
Earthworks and Site Grading		186	342,147.30	30-Apr-26	30-Jul-26	10-Dec-25		342,147.30	206,792.98	0.60
CON-LEG101-LR-3130	Parcrels Excavation for Roadway [Local – 04]	18	16,556.38	18-May-26	11-Jun-26	10-Dec-25	17-Sep-26	16,556.38	16,556.38	1.00
CON-LEG101-LR-4860	Embankments to the parcels for roads [Local – 04]	21	190,236.60	07-Jul-26	30-Jul-26	14-Dec-25	19-Sep-26	190,236.60	190,236.60	1.00
CON-LEG101-LR-1800	Excavation for Roadway [Local – 04]	15	11,823.62	30-Apr-26	17-May-26			11,823.62	0.00	0.00
CON-LEG101-LR-4420	Embankments to the roads [Local – 04]	21	123,530.70	13-Jun-26	06-Jul-26			123,530.70	0.00	0.00
Asphalt Work		25	351,475.20	20-Aug-26	17-Sep-26			351,475.20	0.00	0.00
CON-LEG101-LR-5630	Subgrade [Local – 04]	12	55,987.20	20-Aug-26	02-Sep-26			55,987.20	0.00	0.00
CON-LEG101-LR-5730	Aggregate base course [Local – 04]	8	69,984.00	05-Sep-26	13-Sep-26			69,984.00	0.00	0.00
CON-LEG101-LR-5830	Prime Coat (MC1) [Local – 04]	2	67,651.20	14-Sep-26	15-Sep-26			67,651.20	0.00	0.00
CON-LEG101-LR-5930	Bituminous Base Course [Local – 04]	2	157,852.80	16-Sep-26	17-Sep-26			157,852.80	0.00	0.00
Electric Works		24	115,297.10	22-Aug-26	17-Sep-26			115,297.10	0.00	0.00
Medium Voltage		24	115,297.10	22-Aug-26	17-Sep-26			115,297.10	0.00	0.00
CON-LEG101-LR-6930	Excavation for Medium Voltage trench [Local – 04]	4	3,259.60	22-Aug-26	25-Aug-26			3,259.60	0.00	0.00
CON-LEG101-LR-7020	Installation of Medium Voltage Cables Duct Banks [Local – 04]	3	4,106.50	26-Aug-26	29-Aug-26			4,106.50	0.00	0.00
CON-LEG101-LR-7110	Installation of Medium Voltage Cables [Local – 04]	6	64,119.00	30-Aug-26	05-Sep-26			64,119.00	0.00	0.00
CON-LEG101-LR-7200	Installation of Straight joints cables [Local – 04]	3	2,016.00	06-Sep-26	08-Sep-26			2,016.00	0.00	0.00
CON-LEG101-LR-7290	Installation of Cable Termination for 13.8 kv 3Cx 500 mm², Al /XLPE/LLI	3	1,596.00	09-Sep-26	12-Sep-26			1,596.00	0.00	0.00
CON-LEG101-LR-7380	Installation of Medium Voltage Switchgears [Local – 04]	2	40,200.00	13-Sep-26	14-Sep-26			40,200.00	0.00	0.00
CON-LEG101-LR-7730	Installation of Cable Termination [Local – 04]	3	0.00	15-Sep-26	17-Sep-26			0.00	0.00	0.00

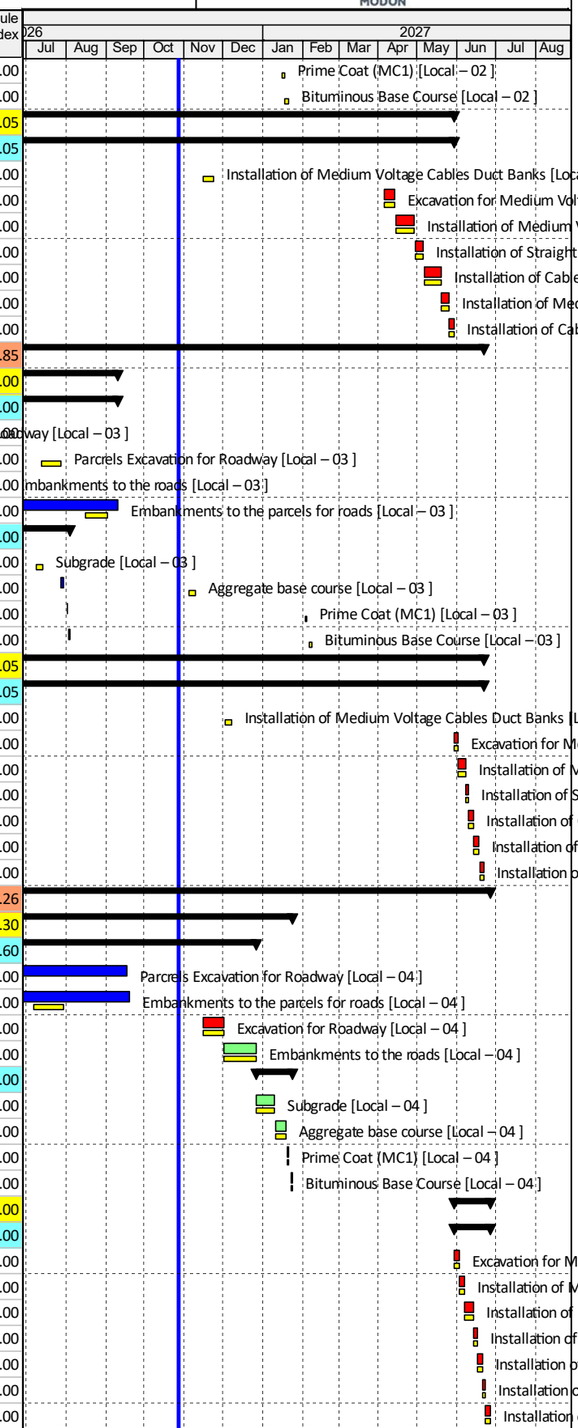


© Oracle Corporation

Activity ID	Activity Name	Original Duration	Budgeted Total Cost	BL Project Start	BL Project Finish	Actual Start	Actual Finish	Planned Value Cost	Earned Value Cost	Schedule Performance Index
Local – 05		363	1,337,737.46	18-May-26	17-Sep-26	04-Dec-25		1,337,737.46	1,030,140.46	0.77
Road Works		142	1,012,351.36	18-May-26	17-Sep-26	04-Dec-25	09-Sep-26	1,012,351.36	1,012,351.36	1.00
Earthworks and Site Grading		110	409,824.32	18-May-26	17-Aug-26	04-Dec-25	09-Sep-26	409,824.32	409,824.32	1.00
CON-LEG101-LR-1900	Excavation for Roadway [Local – 05]	21	17,735.44	18-May-26	15-Jun-26	30-Dec-25	01-Jan-26	17,735.44	17,735.44	1.00
CON-LEG101-LR-4520	Embankments to the roads [Local – 05]	18	185,295.90	11-Jul-26	30-Jul-26	03-Jan-26	20-Jan-26	185,295.90	185,295.90	1.00
CON-LEG101-LR-4930	Embankments to the parcels for roads [Local – 05]	15	190,236.60	01-Aug-26	17-Aug-26	07-Dec-25	09-Jul-26	190,236.60	190,236.60	1.00
CON-LEG101-LR-3190	Parcrels Excavation for Roadway [Local – 05]	21	16,556.38	16-Jun-26	09-Jul-26	04-Dec-25	09-Sep-26	16,556.38	16,556.38	1.00
Asphalt Work		37	602,527.04	30-Aug-26	17-Sep-26	12-Jan-26	23-Jun-26	602,527.04	602,527.04	1.00
CON-LEG101-LR-5640	Subgrade [Local – 05]	10	95,978.24	30-Aug-26	09-Sep-26	12-Jan-26	10-Feb-26	95,978.24	95,978.24	1.00
CON-LEG101-LR-5740	Aggregate base course [Local – 05]	4	119,973.00	12-Sep-26	15-Sep-26	31-May-26	21-Jun-26	119,973.00	119,973.00	1.00
CON-LEG101-LR-5840	Prime Coat (MC1) [Local – 05]	2	115,971.00	16-Sep-26	17-Sep-26	11-Jun-26	22-Jun-26	115,971.00	115,971.00	1.00
CON-LEG101-LR-5940	Bituminous Base Course [Local – 05]	2	270,604.80	16-Sep-26	17-Sep-26	15-Jun-26	23-Jun-26	270,604.80	270,604.80	1.00
Electrical Works		148	325,386.10	30-Aug-26	17-Sep-26	02-May-26		325,386.10	17,789.10	0.05
Medium Voltage		148	325,386.10	30-Aug-26	17-Sep-26	02-May-26		325,386.10	17,789.10	0.05
CON-LEG101-LR-7030	Installation of Medium Voltage Cables Duct Banks [Local – 05]	2	17,789.10	03-Sep-26	05-Sep-26	02-May-26	07-May-26	17,789.10	17,789.10	1.00
CON-LEG101-LR-6940	Excavation for Medium Voltage trench [Local – 05]	4	14,124.00	30-Aug-26	02-Sep-26			14,124.00	0.00	0.00
CON-LEG101-LR-7120	Installation of Medium Voltage Cables [Local – 05]	4	277,849.00	06-Sep-26	09-Sep-26			277,849.00	0.00	0.00
CON-LEG101-LR-7210	Installation of Straight joints cables [Local – 05]	2	8,792.00	10-Sep-26	12-Sep-26			8,792.00	0.00	0.00
CON-LEG101-LR-7300	Installation of Cable Termination for 13.8 kv 3Cx 500 mm², Al /XLPE/LLI	2	6,832.00	13-Sep-26	14-Sep-26			6,832.00	0.00	0.00
CON-LEG101-LR-7390	Installation of Medium Voltage Switchgears [Local – 05]	2	0.00	15-Sep-26	16-Sep-26			0.00	0.00	0.00
CON-LEG101-LR-7740	Installation of Cable Termination [Local – 05]	3	0.00	15-Sep-26	17-Sep-26			0.00	0.00	0.00
Local – 06		341	1,048,514.20	16-Jun-26	17-Sep-26	08-Dec-25		1,048,514.20	760,253.60	0.73
Road Works		118	743,831.90	16-Jun-26	17-Sep-26	08-Dec-25	20-Aug-26	743,831.90	743,831.90	1.00
Earthworks and Site Grading		101	342,147.30	16-Jun-26	31-Aug-26	08-Dec-25	20-Aug-26	342,147.30	342,147.30	1.00
CON-LEG101-LR-4540	Embankments to the roads [Local – 06]	20	123,530.70	26-Jul-26	17-Aug-26	31-Dec-25	01-Jan-26	123,530.70	123,530.70	1.00
CON-LEG101-LR-1990	Excavation for Roadway [Local – 06]	14	11,823.62	16-Jun-26	01-Jul-26	29-Dec-25	05-Jan-26	11,823.62	11,823.62	1.00
CON-LEG101-LR-3290	Parcrels Excavation for Roadway [Local – 06]	20	16,556.38	02-Jul-26	25-Jul-26	08-Dec-25	19-Aug-26	16,556.38	16,556.38	1.00
CON-LEG101-LR-5000	Embankments to the parcels for roads [Local – 06]	12	190,236.60	18-Aug-26	31-Aug-26	14-Dec-25	20-Aug-26	190,236.60	190,236.60	1.00
Asphalt Work		12	401,684.60	01-Sep-26	17-Sep-26	13-Jan-26	06-Jul-26	401,684.60	401,684.60	1.00
CON-LEG101-LR-5650	Subgrade [Local – 06]	6	63,985.60	01-Sep-26	07-Sep-26	13-Jan-26	25-Jan-26	63,985.60	63,985.60	1.00
CON-LEG101-LR-5750	Aggregate base course [Local – 06]	4	79,981.80	08-Sep-26	12-Sep-26	27-Jun-26	29-Jun-26	79,981.80	79,981.80	1.00
CON-LEG101-LR-5850	Prime Coat (MC1) [Local – 06]	2	77,314.00	13-Sep-26	14-Sep-26	01-Jul-26	02-Jul-26	77,314.00	77,314.00	1.00
CON-LEG101-LR-5950	Bituminous Base Course [Local – 06]	3	180,403.20	15-Sep-26	17-Sep-26	04-Jul-26	06-Jul-26	180,403.20	180,403.20	1.00
Electrical Works		122	304,682.30	31-Aug-26	17-Sep-26	17-Jun-26		304,682.30	16,421.70	0.05
Medium Voltage		122	304,682.30	31-Aug-26	17-Sep-26	17-Jun-26		304,682.30	16,421.70	0.05
CON-LEG101-LR-7040	Installation of Medium Voltage Cables Duct Banks [Local – 06]	3	16,421.70	03-Sep-26	06-Sep-26	17-Jun-26	18-Jun-26	16,421.70	16,421.70	1.00
CON-LEG101-LR-6950	Excavation for Medium Voltage trench [Local – 06]	3	13,037.60	31-Aug-26	02-Sep-26			13,037.60	0.00	0.00
CON-LEG101-LR-7130	Installation of Medium Voltage Cables [Local – 06]	3	258,151.00	07-Sep-26	09-Sep-26			258,151.00	0.00	0.00
CON-LEG101-LR-7220	Installation of Straight joints cables [Local – 06]	2	8,092.00	10-Sep-26	12-Sep-26			8,092.00	0.00	0.00
CON-LEG101-LR-7310	Installation of Cable Termination for 13.8 kv 3Cx 500 mm², Al /XLPE/LLI	2	6,300.00	13-Sep-26	14-Sep-26			6,300.00	0.00	0.00
CON-LEG101-LR-7400	Installation of Medium Voltage Switchgears [Local – 06]	2	0.00	15-Sep-26	16-Sep-26			0.00	0.00	0.00
CON-LEG101-LR-7750	Installation of Cable Termination [Local – 06]	3	2,680.00	15-Sep-26	17-Sep-26			2,680.00	0.00	0.00
Local – 07		365	383,519.26	02-Jul-26	17-Sep-26	07-Dec-25		383,519.26	351,696.13	0.92
Road Works		128	354,133.46	02-Jul-26	17-Sep-26	07-Dec-25		354,133.46	350,328.73	0.99
Earthworks and Site Grading		126	251,910.98	02-Jul-26	31-Aug-26	07-Dec-25		251,910.98	248,106.25	0.98
CON-LEG101-LR-3380	Parcrels Excavation for Roadway [Local – 07]	14	16,556.38	14-Jul-26	29-Jul-26	07-Dec-25	10-Dec-25	16,556.38	16,556.38	1.00
CON-LEG101-LR-2080	Excavation for Roadway [Local – 07]	10	3,941.20	02-Jul-26	13-Jul-26	01-Jan-26	07-Jan-26	3,941.20	3,941.20	1.00
CON-LEG101-LR-4550	Embankments to the roads [Local – 07]	14	41,176.80	30-Jul-26	15-Aug-26	08-Jan-26	24-Jan-26	41,176.80	41,176.80	1.00
CON-LEG101-LR-5070	Embankments to the parcels for roads [Local – 07]	14	190,236.60	16-Aug-26	31-Aug-26	11-Dec-25		190,236.60	186,431.87	0.98
Asphalt Work		33	102,222.48	01-Sep-26	17-Sep-26	24-Jan-26	30-Jun-26	102,222.48	102,222.48	1.00
CON-LEG101-LR-5660	Subgrade [Local – 07]	5	15,996.48	01-Sep-26	06-Sep-26	24-Jan-26	26-Jan-26	15,996.48	15,996.48	1.00
CON-LEG101-LR-5760	Aggregate base course [Local – 07]	4	21,793.80	07-Sep-26	10-Sep-26	21-Jun-26	23-Jun-26	21,793.80	21,793.80	1.00
CON-LEG101-LR-5860	Prime Coat (MC1) [Local – 07]	3	19,331.40	12-Sep-26	14-Sep-26	27-Jun-26	28-Jun-26	19,331.40	19,331.40	1.00

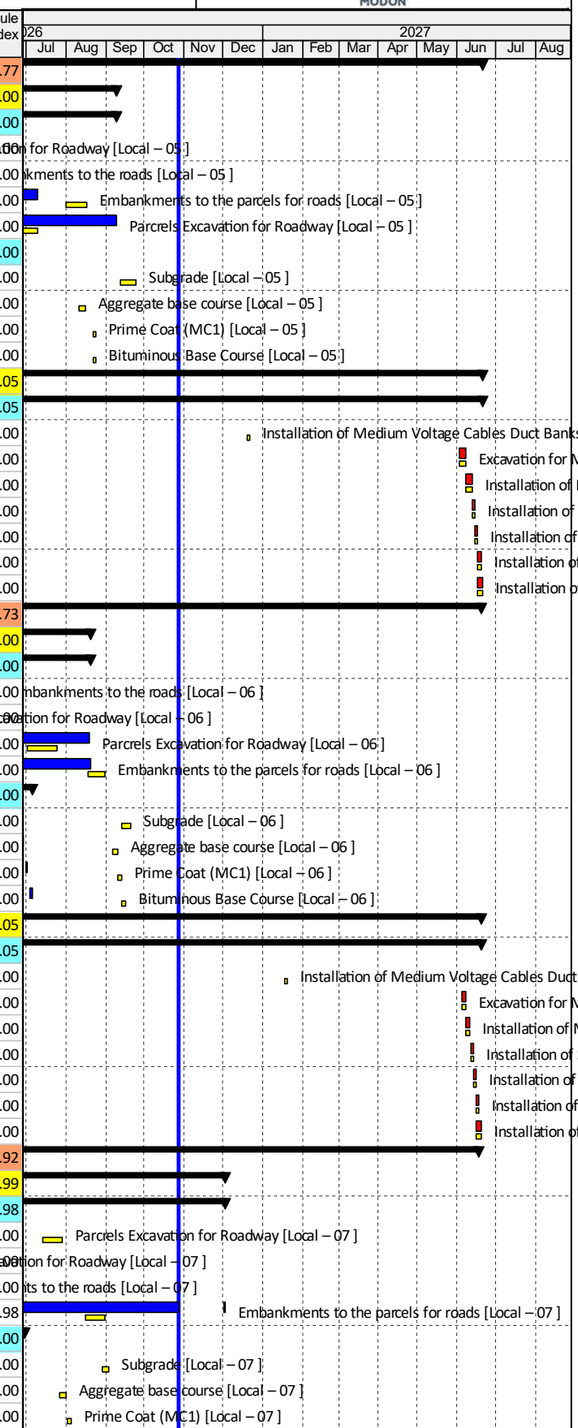


© Oracle Corporation

Activity ID	Activity Name	Original Duration	Budgeted Total Cost	BL Project Start	BL Project Finish	Actual Start	Actual Finish	Planned Value Cost	Earned Value Cost	Schedule Performance Index
CON-LEG101-LR-5960	Bituminous Base Course [Local – 07]	3	45,100.80	15-Sep-26	17-Sep-26	27-Jun-26	30-Jun-26	45,100.80	45,100.80	1.00
Electrical Works		133	29,385.80	01-Sep-26	17-Sep-26	20-May-26		29,385.80	1,367.40	0.05
Medium Voltage		133	29,385.80	01-Sep-26	17-Sep-26	20-May-26		29,385.80	1,367.40	0.05
CON-LEG101-LR-7050	Installation of Medium Voltage Cables Duct Banks [Local – 07]	3	1,367.40	05-Sep-26	07-Sep-26	20-May-26	21-May-26	1,367.40	1,367.40	1.00
CON-LEG101-LR-6960	Excavation for Medium Voltage trench [Local – 07]	3	1,086.40	01-Sep-26	03-Sep-26			1,086.40	0.00	0.00
CON-LEG101-LR-7140	Installation of Medium Voltage Cables [Local – 07]	3	23,048.00	08-Sep-26	10-Sep-26			23,048.00	0.00	0.00
CON-LEG101-LR-7230	Installation of Straight joints cables [Local – 07]	2	672.00	12-Sep-26	13-Sep-26			672.00	0.00	0.00
CON-LEG101-LR-7320	Installation of Cable Termination for 13.8 kv 3Cx 500 mm², Al /XLPE/LLI	2	532.00	14-Sep-26	15-Sep-26			532.00	0.00	0.00
CON-LEG101-LR-7410	Installation of Medium Voltage Switchgears [Local – 07]	2	0.00	16-Sep-26	17-Sep-26			0.00	0.00	0.00
CON-LEG101-LR-7760	Installation of Cable Termination [Local – 07]	2	2,680.00	16-Sep-26	17-Sep-26			2,680.00	0.00	0.00
Local – 08		91	839,164.80	03-Jun-26	17-Sep-26	23-Dec-25	03-Aug-26	839,164.80	839,164.80	1.00
Road Works		91	839,164.80	03-Jun-26	17-Sep-26	23-Dec-25	03-Aug-26	839,164.80	839,164.80	1.00
Earthworks and Site Grading		46	387,265.32	03-Jun-26	31-Aug-26	23-Dec-25	21-Jul-26	387,265.32	387,265.32	1.00
CON-LEG101-LR-2180	Excavation for Roadway [Local – 08]	10	15,764.84	03-Jun-26	14-Jun-26	07-Apr-26	26-Apr-26	15,764.84	15,764.84	1.00
CON-LEG101-LR-4560	Embankments to the roads [Local – 08]	8	164,707.50	11-Aug-26	19-Aug-26	05-Apr-26	27-Apr-26	164,707.50	164,707.50	1.00
CON-LEG101-LR-3470	Parcrels Excavation for Roadway [Local – 08]	10	16,556.38	30-Jul-26	10-Aug-26	23-Dec-25	20-Jul-26	16,556.38	16,556.38	1.00
CON-LEG101-LR-5140	Embankments to the parcels for roads [Local – 08]	10	190,236.60	20-Aug-26	31-Aug-26	05-Apr-26	21-Jul-26	190,236.60	190,236.60	1.00
Asphalt Work		31	451,899.48	01-Sep-26	17-Sep-26	17-Jun-26	03-Aug-26	451,899.48	451,899.48	1.00
CON-LEG101-LR-5670	Subgrade [Local – 08]	7	71,983.68	01-Sep-26	08-Sep-26	17-Jun-26	30-Jun-26	71,983.68	71,983.68	1.00
CON-LEG101-LR-5770	Aggregate base course [Local – 08]	4	89,979.60	09-Sep-26	13-Sep-26	25-Jul-26	28-Jul-26	89,979.60	89,979.60	1.00
CON-LEG101-LR-5870	Prime Coat (MC1) [Local – 08]	2	86,982.60	14-Sep-26	15-Sep-26	01-Aug-26	01-Aug-26	86,982.60	86,982.60	1.00
CON-LEG101-LR-5970	Bituminous Base Course [Local – 08]	2	202,953.60	16-Sep-26	17-Sep-26	02-Aug-26	03-Aug-26	202,953.60	202,953.60	1.00
Deep Infrastructure network		283	10,009,830.20	01-Apr-26	18-Nov-26	27-Dec-25		9,977,473.03	9,752,639.50	0.98
Local – 01		183	5,883,406.70	01-Apr-26	22-Aug-26	27-Dec-25		5,883,406.70	5,835,170.70	0.99
LOCAL - 01 Segment-01 (From 0+000 to 1+066)		138	1,862,782.60	01-Apr-26	03-Aug-26	27-Dec-25		1,862,782.60	1,832,225.10	0.98
Stormwater Utilities		133	991,086.80	01-Apr-26	03-Aug-26	27-Dec-25		991,086.80	987,228.80	1.00
Pipe Work		85	462,178.50	01-Apr-26	08-Jun-26	27-Dec-25	17-Mar-26	462,178.50	462,178.50	1.00
CON-LEG101-LR-3580	Excavation for Stormwater Utilities Network [Local – 01 Segment-01]	10	92,439.40	01-Apr-26	12-Apr-26	27-Dec-25	22-Jan-26	92,439.40	92,439.40	1.00
CON-LEG101-LR-3680	Granular bedding for Stormwater Utilities Network [Local – 01 Segmen	10	23,105.10	13-Apr-26	23-Apr-26	28-Dec-25	24-Jan-26	23,105.10	23,105.10	1.00
CON-LEG101-LR-3780	Installation of Pipe for Stormwater Utilities Network [Local – 01 Segme	10	207,990.40	05-May-26	16-May-26	30-Dec-25	28-Jan-26	207,990.40	207,990.40	1.00
CON-LEG101-LR-3980	Granular Surround for Stormwater Utilities Network [Local – 01 Segme	4	23,105.10	21-May-26	25-May-26	31-Dec-25	29-Jan-26	23,105.10	23,105.10	1.00
CON-LEG101-LR-3880	Testing for Stormwater Utilities Network [Local – 01 Segment-01]	4	46,216.70	17-May-26	20-May-26	02-Jan-26	12-Mar-26	46,216.70	46,216.70	1.00
CON-LEG101-LR-4090	Installation of Micron Marker Magnetic Tape [Local – 01 Segment-01]	2	23,105.10	26-May-26	01-Jun-26	12-Jan-26	15-Mar-26	23,105.10	23,105.10	1.00
CON-LEG101-LR-4200	Backfilling to Subgrade Elevation [Local – 01 Segment-01]	6	46,216.70	02-Jun-26	08-Jun-26	13-Jan-26	17-Mar-26	46,216.70	46,216.70	1.00
Manhole		86	196,590.00	13-Apr-26	30-Jun-26	27-Dec-25		196,590.00	194,618.00	0.99
CON-LEG101-LR-10890	Excavation of Inlet Manholes [Local – 01 Segment-01]	15	29,675.00	13-Apr-26	29-Apr-26	27-Dec-25	22-Jan-26	29,675.00	29,675.00	1.00
CON-LEG101-LR-10900	PC of Inlet Manholes [Local – 01 Segment-01]	6	19,920.00	30-Apr-26	06-May-26	14-Jan-26	25-Jan-26	19,920.00	19,920.00	1.00
CON-LEG101-LR-4320	Installation of Inlet Manholes [Local – 01 Segment-01]	14	88,685.00	17-May-26	06-Jun-26	17-Jan-26	26-Apr-26	88,685.00	88,685.00	1.00
CON-LEG101-LR-10910	Backfilling of Inlet Manholes [Local – 01 Segment-01]	6	38,590.00	07-Jun-26	13-Jun-26	24-Mar-26	28-Apr-26	38,590.00	38,590.00	1.00
CON-LEG101-LR-10920	Finishing and Testing of Inlet Manholes [Local – 01 Segment-01]	15	19,720.00	14-Jun-26	30-Jun-26	28-Mar-26		19,720.00	17,748.00	0.90
Concrete Chambers/Outfalls		85	332,318.30	14-Jun-26	03-Aug-26	26-Mar-26		332,318.30	330,432.30	0.99
CON-LEG101-LR-10840	Excavation of Concrete chambers [Local – 01 Segment-01]	6	28,200.00	14-Jun-26	20-Jun-26	26-Mar-26	09-Apr-26	28,200.00	28,200.00	1.00
CON-LEG101-LR-10850	PC of Concrete chambers [Local – 01 Segment-01]	2	18,860.00	21-Jun-26	22-Jun-26	01-Apr-26	12-Apr-26	18,860.00	18,860.00	1.00
CON-LEG101-LR-10870	Installation UPVC Pipes to Concrete chambers [Local – 01 Segment-01]	8	145,478.30	07-Jul-26	15-Jul-26	02-Apr-26	21-Apr-26	145,478.30	145,478.30	1.00
CON-LEG101-LR-4430	Installation of Concrete chambers [Local – 01 Segment-01]	12	84,320.00	23-Jun-26	06-Jul-26	13-Apr-26	21-Apr-26	84,320.00	84,320.00	1.00
CON-LEG101-LR-10860	Backfilling to Concrete chambers [Local – 01 Segment-01]	6	36,600.00	16-Jul-26	22-Jul-26	22-Apr-26	25-Apr-26	36,600.00	36,600.00	1.00
CON-LEG101-LR-10880	FInishing and Testing of Concrete chambers [Local – 01 Segment-01]	10	18,860.00	23-Jul-26	03-Aug-26	01-Jul-26		18,860.00	16,974.00	0.90
Sanitary Sewerage		55	871,695.80	13-Apr-26	15-Jun-26	12-Jan-26		871,695.80	844,996.30	0.97
Pipe Work		50	337,705.80	13-Apr-26	15-Jun-26	12-Jan-26	07-Mar-26	337,705.80	337,705.80	1.00
CON-LEG101-LR-2780	Excavation for Sanitary Sewerage Network [Local – 01 Segment-01]	10	66,057.00	13-Apr-26	23-Apr-26	12-Jan-26	24-Jan-26	66,057.00	66,057.00	1.00
CON-LEG101-LR-2870	Granular bedding for Sanitary Sewerage Network [Local – 01 Segmer	4	16,518.70	25-Apr-26	28-Apr-26	13-Jan-26	24-Jan-26	16,518.70	16,518.70	1.00
CON-LEG101-LR-2960	Installation of Pipe for Sanitary Sewerage Network [Local – 01 Segment	10	148,632.70	06-May-26	17-May-26	15-Jan-26	28-Jan-26	148,632.70	148,632.70	1.00
CON-LEG101-LR-3230	Granular Surround for Sanitary Sewerage Network [Local – 01 Segme	4	16,518.70	26-May-26	03-Jun-26	18-Jan-26	29-Jan-26	16,518.70	16,518.70	1.00

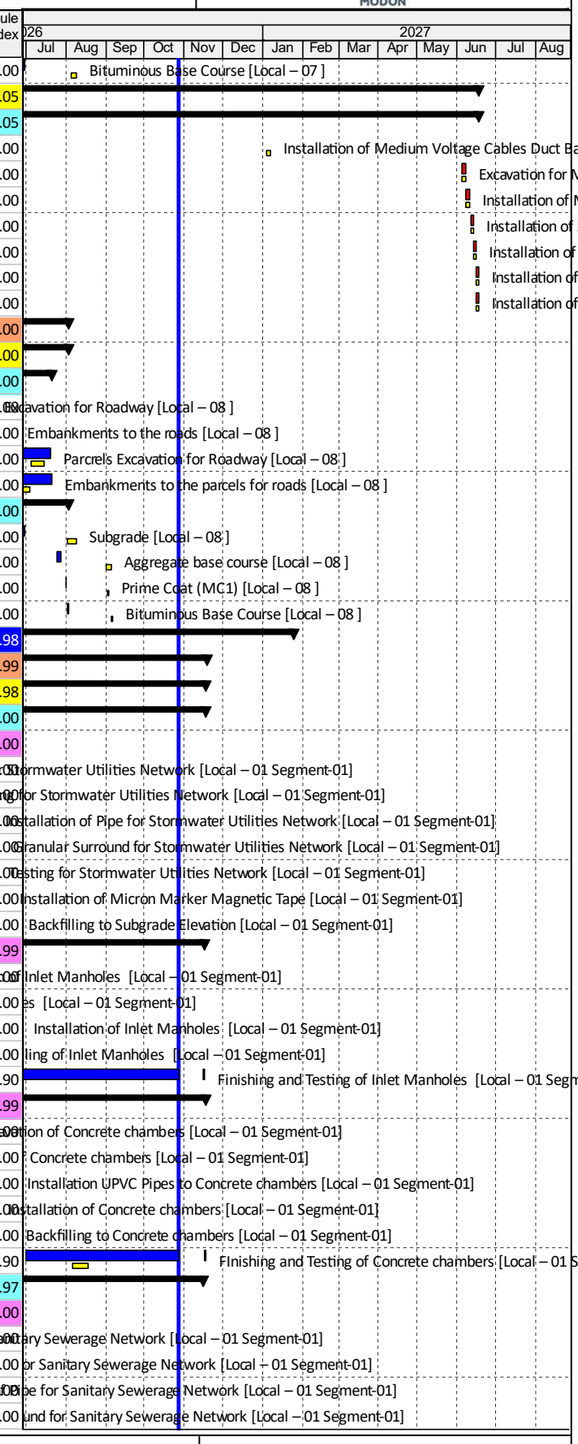


© Oracle Corporation

Activity ID	Activity Name	Original Duration	Budgeted Total Cost	BL Project Start	BL Project Finish	Actual Start	Actual Finish	Planned Value Cost	Earned Value Cost	Schedule Performance Index
CON-LEG101-LR-3140	Concrete encasement, pipe dia 200 and 350 mm [Local – 01 Segmen	3	7,400.80	23-May-26	25-May-26	01-Feb-26	02-Feb-26	7,400.80	7,400.80	1.00
CON-LEG101-LR-3050	Testing for Sanitary Sewerage Network [Local – 01 Segment-01]	4	33,029.60	18-May-26	21-May-26	01-Mar-26	03-Mar-26	33,029.60	33,029.60	1.00
CON-LEG101-LR-3320	Installation of Micron Marker Magnetic Tape [Local – 01 Segment-01]	2	16,518.70	04-Jun-26	06-Jun-26	04-Mar-26	05-Mar-26	16,518.70	16,518.70	1.00
CON-LEG101-LR-3410	Backfilling to Subgrade Elevation [Local – 01 Segment-01]	8	33,029.60	07-Jun-26	15-Jun-26	04-Mar-26	07-Mar-26	33,029.60	33,029.60	1.00
Manhole		20	533,990.00	18-May-26	14-Jun-26	13-Jan-26		533,990.00	507,290.50	0.95
CON-LEG101-LR-3500	Installation of Fiberglass Manholes [Local – 01 Segment-01]	20	533,990.00	18-May-26	14-Jun-26	13-Jan-26		533,990.00	507,290.50	0.95
LOCAL - 01 Segment-02 (From 1+066 to 2+133)		158	1,908,422.30	27-Apr-26	15-Aug-26	21-Jan-26		1,908,422.30	1,906,407.30	1.00
Stormwater Utilities		158	1,390,459.30	27-Apr-26	15-Aug-26	21-Jan-26		1,390,459.30	1,389,516.30	1.00
Pipe Work		106	624,416.00	27-Apr-26	14-Jun-26	21-Jan-26	14-May-26	624,416.00	624,416.00	1.00
CON-LEG101-LR-3590	Excavation for Stormwater Utilities Network [Local – 01 Segment-02]	10	124,847.00	27-Apr-26	07-May-26	21-Jan-26	10-Feb-26	124,847.00	124,847.00	1.00
CON-LEG101-LR-3690	Granular bedding for Stormwater Utilities Network [Local – 01 Segmen	4	31,243.00	09-May-26	12-May-26	24-Jan-26	12-Feb-26	31,243.00	31,243.00	1.00
CON-LEG101-LR-3790	Installation of Pipe for Stormwater Utilities Network [Local – 01 Segme	8	281,005.00	13-May-26	21-May-26	28-Jan-26	09-Apr-26	281,005.00	281,005.00	1.00
CON-LEG101-LR-3990	Granular Surround for Stormwater Utilities Network [Local – 01 Segme	4	31,220.00	01-Jun-26	04-Jun-26	29-Jan-26	11-Apr-26	31,220.00	31,220.00	1.00
CON-LEG101-LR-3890	Testing for Stormwater Utilities Network [Local – 01 Segment-02]	4	62,440.50	23-May-26	26-May-26	01-Mar-26	12-May-26	62,440.50	62,440.50	1.00
CON-LEG101-LR-4100	Installation of Micron Marker Magnetic Tape [Local – 01 Segment-02]	2	31,220.00	06-Jun-26	07-Jun-26	11-Mar-26	13-May-26	31,220.00	31,220.00	1.00
CON-LEG101-LR-4210	Backfilling to Subgrade Elevation [Local – 01 Segment-02]	6	62,440.50	08-Jun-26	14-Jun-26	12-Mar-26	14-May-26	62,440.50	62,440.50	1.00
Manhole		75	373,475.00	09-May-26	28-Jun-26	21-Jan-26	24-Aug-26	373,475.00	373,475.00	1.00
CON-LEG101-LR-10930	Excavation of Inlet Manholes [Local – 01 Segment-02]	6	56,015.00	09-May-26	14-May-26	21-Jan-26	10-Mar-26	56,015.00	56,015.00	1.00
CON-LEG101-LR-10940	PC of Inlet Manholes [Local – 01 Segment-02]	3	37,400.00	16-May-26	18-May-26	11-Feb-26	25-Mar-26	37,400.00	37,400.00	1.00
CON-LEG101-LR-10960	Backfilling of Inlet Manholes [Local – 01 Segment-02]	6	74,290.00	08-Jun-26	14-Jun-26	26-Mar-26	27-Apr-26	74,290.00	74,290.00	1.00
CON-LEG101-LR-4330	Installation of Inlet Manholes [Local – 01 Segment-02]	10	168,370.00	23-May-26	07-Jun-26	15-Feb-26	30-Apr-26	168,370.00	168,370.00	1.00
CON-LEG101-LR-10970	Finishing and Testing of Inlet Manholes [Local – 01 Segment-02]	12	37,400.00	15-Jun-26	28-Jun-26	28-Mar-26	24-Aug-26	37,400.00	37,400.00	1.00
Concrete Chambers/Outfalls		91	392,568.30	15-Jun-26	15-Aug-26	14-Apr-26		392,568.30	391,625.30	1.00
CON-LEG101-LR-10980	Excavation of Concrete chambers [Local – 01 Segment-02]	10	28,200.00	15-Jun-26	25-Jun-26	14-Apr-26	29-Apr-26	28,200.00	28,200.00	1.00
CON-LEG101-LR-10990	PC of Concrete chambers [Local – 01 Segment-02]	2	18,860.00	27-Jun-26	28-Jun-26	20-Apr-26	30-Apr-26	18,860.00	18,860.00	1.00
CON-LEG101-LR-11010	Installation UPVC Pipes to Concrete chambers [Local – 01 Segment-02]	8	174,958.30	16-Jul-26	25-Jul-26	21-Apr-26	05-May-26	174,958.30	174,958.30	1.00
CON-LEG101-LR-4440	Installation of Concrete chambers [Local – 01 Segment-02]	15	114,470.00	29-Jun-26	15-Jul-26	21-Apr-26	05-May-26	114,470.00	114,470.00	1.00
CON-LEG101-LR-11020	Backfilling to Concrete chambers [Local – 01 Segment-02]	6	37,220.00	26-Jul-26	01-Aug-26	25-Apr-26	07-May-26	37,220.00	37,220.00	1.00
CON-LEG101-LR-11030	FInishing and Testing of Concrete chambers [Local – 01 Segment-02]	10	18,860.00	04-Aug-26	15-Aug-26	04-Jul-26		18,860.00	17,917.00	0.95
Sanitary Sewerage		40	517,963.00	27-Apr-26	16-Jun-26	11-Mar-26		517,963.00	516,891.00	1.00
Pipe Work		34	464,363.00	27-Apr-26	14-Jun-26	11-Mar-26	09-May-26	464,363.00	464,363.00	1.00
CON-LEG101-LR-2790	Excavation for Sanitary Sewerage Network [Local – 01 Segment-02]	7	91,211.00	27-Apr-26	04-May-26	11-Mar-26	07-Apr-26	91,211.00	91,211.00	1.00
CON-LEG101-LR-2880	Granular bedding for Sanitary Sewerage Network [Local – 01 Segmer	4	22,791.20	05-May-26	09-May-26	17-Mar-26	08-Apr-26	22,791.20	22,791.20	1.00
CON-LEG101-LR-2970	Installation of Pipe for Sanitary Sewerage Network [Local – 01 Segment	8	205,207.20	10-May-26	18-May-26	24-Mar-26	09-Apr-26	205,207.20	205,207.20	1.00
CON-LEG101-LR-3150	Concrete encasement, pipe dia 200 and 350 mm [Local – 01 Segmen	3	8,375.00	24-May-26	26-May-26	02-Apr-26	11-Apr-26	8,375.00	8,375.00	1.00
CON-LEG101-LR-3240	Granular Surround for Sanitary Sewerage Network [Local – 01 Segme	4	22,790.70	01-Jun-26	04-Jun-26	04-Apr-26	11-Apr-26	22,790.70	22,790.70	1.00
CON-LEG101-LR-3060	Testing for Sanitary Sewerage Network [Local – 01 Segment-02]	4	45,598.60	19-May-26	23-May-26	01-Apr-26	06-May-26	45,598.60	45,598.60	1.00
CON-LEG101-LR-3330	Installation of Micron Marker Magnetic Tape [Local – 01 Segment-02]	2	22,790.70	06-Jun-26	07-Jun-26	11-Apr-26	07-May-26	22,790.70	22,790.70	1.00
CON-LEG101-LR-3420	Backfilling to Subgrade Elevation [Local – 01 Segment-02]	6	45,598.60	08-Jun-26	14-Jun-26	12-Apr-26	09-May-26	45,598.60	45,598.60	1.00
Manhole		21	53,600.00	19-May-26	16-Jun-26	11-Mar-26		53,600.00	52,528.00	0.98
CON-LEG101-LR-3510	Installation of Fiberglass Manholes [Local – 01 Segment-02]	21	53,600.00	19-May-26	16-Jun-26	11-Mar-26		53,600.00	52,528.00	0.98
LOCAL - 01 Segment-03 (From 2+133 to 3+200)		159	2,112,201.80	09-May-26	22-Aug-26	01-Jan-26		2,112,201.80	2,096,538.30	0.99
Stormwater Utilities		159	1,589,588.30	09-May-26	22-Aug-26	01-Jan-26		1,589,588.30	1,586,085.30	1.00
Pipe Work		68	745,640.00	09-May-26	25-Jun-26	01-Jan-26	12-Mar-26	745,640.00	745,640.00	1.00
CON-LEG101-LR-3600	Excavation for Stormwater Utilities Network [Local – 01 Segment-03]	10	149,121.50	09-May-26	19-May-26	01-Jan-26	10-Feb-26	149,121.50	149,121.50	1.00
CON-LEG101-LR-3700	Granular bedding for Stormwater Utilities Network [Local – 01 Segmen	4	37,277.50	20-May-26	24-May-26	03-Jan-26	12-Feb-26	37,277.50	37,277.50	1.00
CON-LEG101-LR-3800	Installation of Pipe for Stormwater Utilities Network [Local – 01 Segme	8	335,546.00	25-May-26	07-Jun-26	04-Jan-26	14-Feb-26	335,546.00	335,546.00	1.00
CON-LEG101-LR-4000	Granular Surround for Stormwater Utilities Network [Local – 01 Segme	4	37,277.50	13-Jun-26	16-Jun-26	05-Jan-26	15-Feb-26	37,277.50	37,277.50	1.00
CON-LEG101-LR-3900	Testing for Stormwater Utilities Network [Local – 01 Segment-03]	4	74,570.00	08-Jun-26	11-Jun-26	06-Jan-26	02-Mar-26	74,570.00	74,570.00	1.00
CON-LEG101-LR-4110	Installation of Micron Marker Magnetic Tape [Local – 01 Segment-03]	2	37,277.50	17-Jun-26	18-Jun-26	25-Feb-26	11-Mar-26	37,277.50	37,277.50	1.00
CON-LEG101-LR-4220	Backfilling to Subgrade Elevation [Local – 01 Segment-03]	6	74,570.00	20-Jun-26	25-Jun-26	25-Feb-26	12-Mar-26	74,570.00	74,570.00	1.00
Manhole		79	510,650.00	20-May-26	07-Jul-26	01-Jan-26		510,650.00	508,090.00	0.99
CON-LEG101-LR-11040	Excavation of Inlet Manholes [Local – 01 Segment-03]	6	76,850.00	20-May-26	26-May-26	01-Jan-26	10-Feb-26	76,850.00	76,850.00	1.00

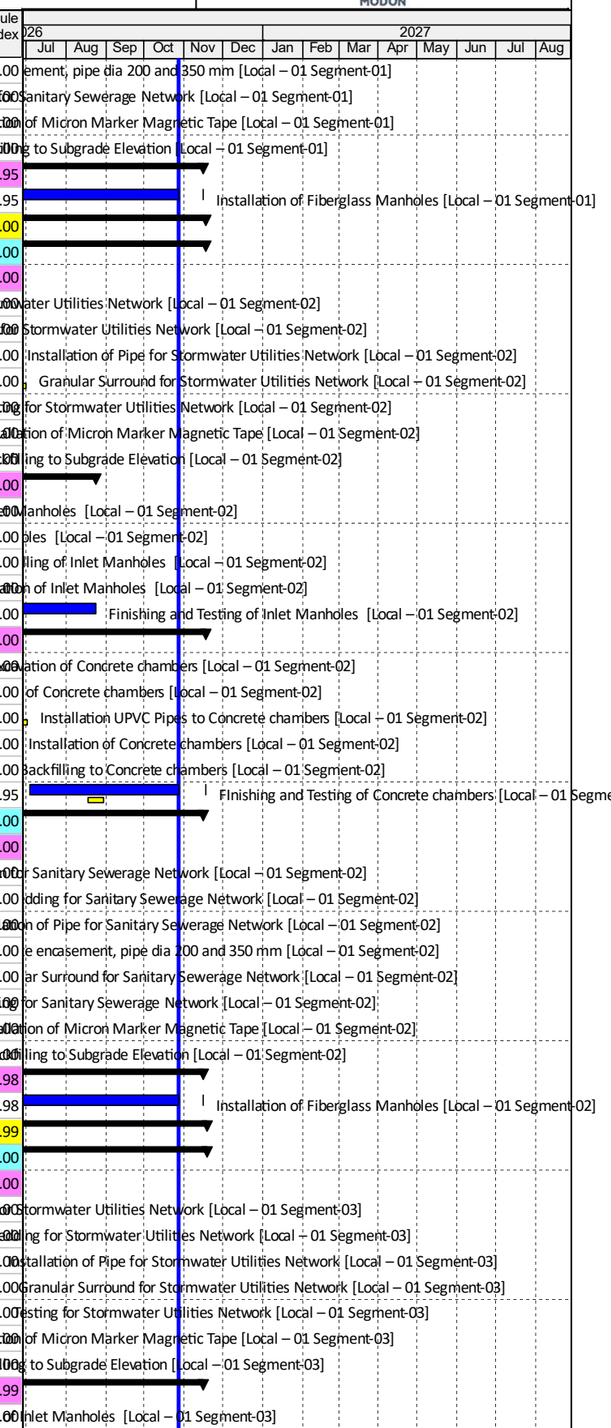


© Oracle Corporation

Activity ID	Activity Name	Original Duration	Budgeted Total Cost	BL Project Start	BL Project Finish	Actual Start	Actual Finish	Planned Value Cost	Earned Value Cost	Schedule Performance Index
CON-LEG101-LR-11050	PC of Inlet Manholes [Local – 01 Segment-03]	3	51,200.00	01-Jun-26	03-Jun-26	15-Jan-26	14-Feb-26	51,200.00	51,200.00	1.00
CON-LEG101-LR-4340	Installation of Inlet Manholes [Local – 01 Segment-03]	14	229,640.00	08-Jun-26	23-Jun-26	21-Jan-26	01-Jun-26	229,640.00	229,640.00	1.00
CON-LEG101-LR-11060	Backfilling of Inlet Manholes [Local – 01 Segment-03]	6	101,760.00	24-Jun-26	30-Jun-26	26-Mar-26	04-Jun-26	101,760.00	101,760.00	1.00
CON-LEG101-LR-11070	Finishing and Testing of Inlet Manholes [Local – 01 Segment-03]	6	51,200.00	01-Jul-26	07-Jul-26	28-Mar-26		51,200.00	48,640.00	0.95
Concrete Chambers/Outfalls		104	333,298.30	24-Jun-26	22-Aug-26	21-Apr-26		333,298.30	332,355.30	1.00
CON-LEG101-LR-11080	Excavation of Concrete chambers [Local – 01 Segment-03]	6	28,200.00	24-Jun-26	30-Jun-26	21-Apr-26	01-Jul-26	28,200.00	28,200.00	1.00
CON-LEG101-LR-11090	PC of Concrete chambers [Local – 01 Segment-03]	2	18,860.00	01-Jul-26	02-Jul-26	23-Apr-26	01-Jul-26	18,860.00	18,860.00	1.00
CON-LEG101-LR-11110	Installation UPVC Pipes to Concrete chambers [Local – 01 Segment-03]	8	145,478.30	15-Jul-26	23-Jul-26	20-May-26	02-Jul-26	145,478.30	145,478.30	1.00
CON-LEG101-LR-4450	Installation of Concrete chambers [Local – 01 Segment-03]	10	84,320.00	04-Jul-26	14-Jul-26	19-May-26	02-Jul-26	84,320.00	84,320.00	1.00
CON-LEG101-LR-11120	Backfilling to Concrete chambers [Local – 01 Segment-03]	6	37,580.00	25-Jul-26	30-Jul-26	01-Jun-26	04-Jul-26	37,580.00	37,580.00	1.00
CON-LEG101-LR-11130	FInishing and Testing of Concrete chambers [Local – 01 Segment-03]	6	18,860.00	16-Aug-26	22-Aug-26	19-Aug-26		18,860.00	17,917.00	0.95
Sanitary Sewerage		44	522,613.50	20-May-26	14-Jul-26	01-Apr-26		522,613.50	510,453.00	0.98
Pipe Work		25	279,403.50	20-May-26	13-Jul-26	01-Apr-26	24-May-26	279,403.50	279,403.50	1.00
CON-LEG101-LR-2800	Excavation for Sanitary Sewerage Network [Local – 01 Segment-03]	10	55,873.00	20-May-26	04-Jun-26	01-Apr-26	27-Apr-26	55,873.00	55,873.00	1.00
CON-LEG101-LR-2890	Granular bedding for Sanitary Sewerage Network [Local – 01 Segmer	4	14,007.70	06-Jun-26	09-Jun-26	07-Apr-26	29-Apr-26	14,007.70	14,007.70	1.00
CON-LEG101-LR-2980	Installation of Pipe for Sanitary Sewerage Network [Local – 01 Segment	10	125,713.20	10-Jun-26	21-Jun-26	08-Apr-26	30-Apr-26	125,713.20	125,713.20	1.00
CON-LEG101-LR-3070	Testing for Sanitary Sewerage Network [Local – 01 Segment-03]	4	27,937.60	22-Jun-26	25-Jun-26	21-Apr-26	19-May-26	27,937.60	27,937.60	1.00
CON-LEG101-LR-3250	Granular Surround for Sanitary Sewerage Network [Local – 01 Segme	4	13,967.20	30-Jun-26	04-Jul-26	23-Apr-26	20-May-26	13,967.20	13,967.20	1.00
CON-LEG101-LR-3160	Concrete encasement, pipe dia 200 and 350 mm [Local – 01 Segmen	3	0.00	27-Jun-26	29-Jun-26	22-Apr-26	20-May-26	0.00	0.00	0.00
CON-LEG101-LR-3340	Installation of Micron Marker Magnetic Tape [Local – 01 Segment-03]	2	13,967.20	05-Jul-26	06-Jul-26	25-Apr-26	21-May-26	13,967.20	13,967.20	1.00
CON-LEG101-LR-3430	Backfilling to Subgrade Elevation [Local – 01 Segment-03]	6	27,937.60	07-Jul-26	13-Jul-26	26-Apr-26	24-May-26	27,937.60	27,937.60	1.00
Manhole		20	243,210.00	22-Jun-26	14-Jul-26	01-Apr-26		243,210.00	231,049.50	0.95
CON-LEG101-LR-3520	Installation of Fiberglass Manholes [Local – 01 Segment-03]	20	243,210.00	22-Jun-26	14-Jul-26	01-Apr-26		243,210.00	231,049.50	0.95
Local – 02		137	937,781.20	14-Apr-26	01-Sep-26	12-Feb-26		937,781.20	927,171.70	0.99
Stormwater Utilities		137	618,274.30	14-Apr-26	01-Sep-26	19-Feb-26		618,274.30	616,944.30	1.00
Pipe Work		51	254,238.50	14-Apr-26	06-Jun-26	19-Feb-26	28-Apr-26	254,238.50	254,238.50	1.00
CON-LEG101-LR-3610	Excavation for Stormwater Utilities Network [Local – 02]	6	50,832.00	14-Apr-26	20-Apr-26	19-Feb-26	28-Mar-26	50,832.00	50,832.00	1.00
CON-LEG101-LR-3710	Granular bedding for Stormwater Utilities Network [Local – 02]	4	12,710.00	21-Apr-26	25-Apr-26	25-Feb-26	22-Apr-26	12,710.00	12,710.00	1.00
CON-LEG101-LR-3810	Installation of Pipe for Stormwater Utilities Network [Local – 02]	8	114,420.50	05-May-26	13-May-26	26-Feb-26	23-Apr-26	114,420.50	114,420.50	1.00
CON-LEG101-LR-3910	Testing for Stormwater Utilities Network [Local – 02]	4	25,428.00	14-May-26	18-May-26	11-Apr-26	25-Apr-26	25,428.00	25,428.00	1.00
CON-LEG101-LR-4010	Granular Surround for Stormwater Utilities Network [Local – 02]	4	12,710.00	19-May-26	23-May-26	09-Apr-26	26-Apr-26	12,710.00	12,710.00	1.00
CON-LEG101-LR-4120	Installation of Micron Marker Magnetic Tape [Local – 02]	2	12,710.00	24-May-26	25-May-26	21-Apr-26	27-Apr-26	12,710.00	12,710.00	1.00
CON-LEG101-LR-4230	Backfilling to Subgrade Elevation [Local – 02]	6	25,428.00	26-May-26	06-Jun-26	22-Apr-26	28-Apr-26	25,428.00	25,428.00	1.00
Manhole		111	169,330.00	21-Apr-26	19-Jul-26	19-Feb-26		169,330.00	168,485.00	1.00
CON-LEG101-LR-11140	Excavation of Inlet Manholes [Local – 02]	10	25,350.00	21-Apr-26	02-May-26	19-Feb-26	28-Mar-26	25,350.00	25,350.00	1.00
CON-LEG101-LR-11150	PC of Inlet Manholes [Local – 02]	5	16,900.00	03-May-26	07-May-26	25-Mar-26	29-Mar-26	16,900.00	16,900.00	1.00
CON-LEG101-LR-4350	Installation of Inlet Manholes [Local – 02]	14	76,215.00	14-May-26	03-Jun-26	26-Mar-26	04-Jun-26	76,215.00	76,215.00	1.00
CON-LEG101-LR-11170	Backfilling of Inlet Manholes [Local – 02]	6	33,965.00	04-Jun-26	10-Jun-26	15-Apr-26	07-Jun-26	33,965.00	33,965.00	1.00
CON-LEG101-LR-11180	Finishing and Testing of Inlet Manholes [Local – 02]	10	16,900.00	08-Jul-26	19-Jul-26	05-Jul-26		16,900.00	16,055.00	0.95
Concrete Chambers/Outfalls		71	194,705.80	20-Jul-26	01-Sep-26	02-May-26		194,705.80	194,220.80	1.00
CON-LEG101-LR-11190	Excavation of Concrete chambers [Local – 02]	6	14,680.00	20-Jul-26	26-Jul-26	02-May-26	10-May-26	14,680.00	14,680.00	1.00
CON-LEG101-LR-11200	PC of Concrete chambers [Local – 02]	2	9,700.00	27-Jul-26	28-Jul-26	03-May-26	11-May-26	9,700.00	9,700.00	1.00
CON-LEG101-LR-4460	Installation of Concrete chambers [Local – 02]	8	44,180.00	29-Jul-26	06-Aug-26	04-May-26	12-May-26	44,180.00	44,180.00	1.00
CON-LEG101-LR-11210	Installation UPVC Pipes to Concrete chambers [Local – 02]	8	96,985.80	08-Aug-26	16-Aug-26	04-May-26	13-May-26	96,985.80	96,985.80	1.00
CON-LEG101-LR-11220	Backfilling to Concrete chambers [Local – 02]	6	19,460.00	17-Aug-26	23-Aug-26	06-May-26	21-May-26	19,460.00	19,460.00	1.00
CON-LEG101-LR-11230	FInishing and Testing of Concrete chambers [Local – 02]	8	9,700.00	24-Aug-26	01-Sep-26	05-Jul-26		9,700.00	9,215.00	0.95
Sanitary Sewerage		80	319,506.90	21-Apr-26	15-Jun-26	12-Feb-26		319,506.90	310,227.40	0.97
Pipe Work		80	133,916.90	21-Apr-26	14-Jun-26	12-Feb-26	08-Jun-26	133,916.90	133,916.90	1.00
CON-LEG101-LR-2810	Excavation for Sanitary Sewerage Network [Local – 02]	10	22,324.00	21-Apr-26	02-May-26	12-Feb-26	19-May-26	22,324.00	22,324.00	1.00
CON-LEG101-LR-2900	Granular bedding for Sanitary Sewerage Network [Local – 02]	4	5,585.60	03-May-26	06-May-26	19-Feb-26	20-May-26	5,585.60	5,585.60	1.00
CON-LEG101-LR-2990	Installation of Pipe for Sanitary Sewerage Network [Local – 02]	10	50,286.10	07-May-26	18-May-26	21-Feb-26	21-May-26	50,286.10	50,286.10	1.00
CON-LEG101-LR-3260	Granular Surround for Sanitary Sewerage Network [Local – 02]	4	5,585.60	01-Jun-26	04-Jun-26	22-Feb-26	23-May-26	5,585.60	5,585.60	1.00
CON-LEG101-LR-3080	Testing for Sanitary Sewerage Network [Local – 02]	4	11,176.00	19-May-26	23-May-26	31-May-26	31-May-26	11,176.00	11,176.00	1.00

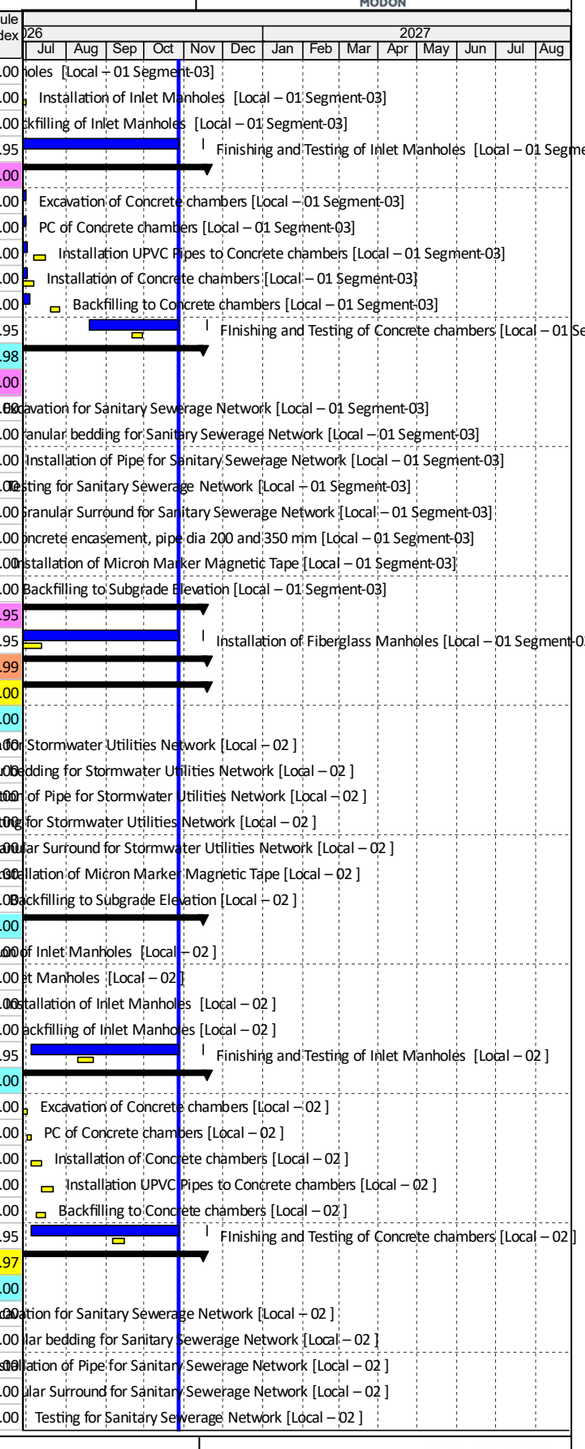


© Oracle Corporation

Activity ID	Activity Name	Original Duration	Budgeted Total Cost	BL Project Start	BL Project Finish	Actual Start	Actual Finish	Planned Value Cost	Earned Value Cost	Schedule Performance Index
CON-LEG101-LR-3170	Concrete encasement, pipe dia 200 and 350 mm [Local – 02]	3	22,198.00	24-May-26	26-May-26	01-Jun-26	02-Jun-26	22,198.00	22,198.00	1.00
CON-LEG101-LR-3350	Installation of Micron Marker Magnetic Tape [Local – 02]	2	5,585.60	06-Jun-26	07-Jun-26	03-Jun-26	04-Jun-26	5,585.60	5,585.60	1.00
CON-LEG101-LR-3440	Backfilling to Subgrade Elevation [Local – 02]	6	11,176.00	08-Jun-26	14-Jun-26	06-Jun-26	08-Jun-26	11,176.00	11,176.00	1.00
Manhole		20	185,590.00	19-May-26	15-Jun-26	12-Feb-26		185,590.00	176,310.50	0.95
CON-LEG101-LR-3530	Installation of Fiberglass Manholes [Local – 02]	20	185,590.00	19-May-26	15-Jun-26	12-Feb-26		185,590.00	176,310.50	0.95
Local – 03		196	172,251.60	30-Apr-26	15-Sep-26	14-Feb-26		172,251.60	169,970.10	0.99
Stormwater Utilities		196	172,251.60	30-Apr-26	15-Sep-26	14-Feb-26		172,251.60	169,970.10	0.99
Pipe Work		70	28,698.00	30-Apr-26	14-Jun-26	14-Feb-26	24-May-26	28,698.00	28,698.00	1.00
CON-LEG101-LR-3620	Excavation for Stormwater Utilities Network [Local – 03]	10	5,742.00	30-Apr-26	11-May-26	14-Feb-26	30-Apr-26	5,742.00	5,742.00	1.00
CON-LEG101-LR-3720	Granular bedding for Stormwater Utilities Network [Local – 03]	3	1,434.00	12-May-26	14-May-26	02-May-26	04-May-26	1,434.00	1,434.00	1.00
CON-LEG101-LR-3820	Installation of Pipe for Stormwater Utilities Network [Local – 03]	8	12,918.00	16-May-26	24-May-26	05-May-26	09-May-26	12,918.00	12,918.00	1.00
CON-LEG101-LR-3920	Testing for Stormwater Utilities Network [Local – 03]	3	2,868.00	25-May-26	01-Jun-26	19-May-26	19-May-26	2,868.00	2,868.00	1.00
CON-LEG101-LR-4020	Granular Surround for Stormwater Utilities Network [Local – 03]	3	1,434.00	02-Jun-26	04-Jun-26	20-May-26	20-May-26	1,434.00	1,434.00	1.00
CON-LEG101-LR-4130	Installation of Micron Marker Magnetic Tape [Local – 03]	2	1,434.00	06-Jun-26	07-Jun-26	21-May-26	21-May-26	1,434.00	1,434.00	1.00
CON-LEG101-LR-4240	Backfilling to Subgrade Elevation [Local – 03]	6	2,868.00	08-Jun-26	14-Jun-26	23-May-26	24-May-26	2,868.00	2,868.00	1.00
Manhole		186	21,030.00	12-May-26	15-Sep-26	14-Feb-26		21,030.00	20,368.50	0.97
CON-LEG101-LR-11240	Excavation of Inlet Manholes [Local – 03]	6	3,225.00	12-May-26	18-May-26	14-Feb-26	30-Apr-26	3,225.00	3,225.00	1.00
CON-LEG101-LR-11250	PC of Inlet Manholes [Local – 03]	3	2,205.00	19-May-26	21-May-26	02-May-26	04-May-26	2,205.00	2,205.00	1.00
CON-LEG101-LR-11260	Installation of Inlet Manholes [Local – 03]	14	9,325.00	23-May-26	11-Jun-26	05-May-26	01-Jun-26	9,325.00	9,325.00	1.00
CON-LEG101-LR-11270	Backfilling of Inlet Manholes [Local – 03]	6	4,070.00	13-Jun-26	18-Jun-26	03-Jun-26	04-Jun-26	4,070.00	4,070.00	1.00
CON-LEG101-LR-11280	Finishing and Testing of Inlet Manholes [Local – 03]	20	2,205.00	24-Aug-26	15-Sep-26	14-Oct-26		2,205.00	1,543.50	0.70
Concrete Chambers/Outfalls		117	122,523.60	13-Jun-26	14-Sep-26	15-Jun-26		122,523.60	120,903.60	0.99
CON-LEG101-LR-11290	Excavation of Concrete chambers [Local – 03]	12	8,160.00	13-Jun-26	25-Jun-26	15-Jun-26	24-Jun-26	8,160.00	8,160.00	1.00
CON-LEG101-LR-11310	Installation of Concrete chambers [Local – 03]	20	24,620.00	02-Jul-26	25-Jul-26	17-Jun-26	25-Jun-26	24,620.00	24,620.00	1.00
CON-LEG101-LR-11300	PC of Concrete chambers [Local – 03]	5	5,400.00	27-Jun-26	01-Jul-26	16-Jun-26	25-Jun-26	5,400.00	5,400.00	1.00
CON-LEG101-LR-11320	Installation UPVC Pipes to Concrete chambers [Local – 03]	10	67,883.60	26-Jul-26	05-Aug-26	18-Jun-26	27-Jun-26	67,883.60	67,883.60	1.00
CON-LEG101-LR-11330	Backfilling to Concrete chambers [Local – 03]	6	11,060.00	06-Aug-26	12-Aug-26	20-Jun-26	30-Jun-26	11,060.00	11,060.00	1.00
CON-LEG101-LR-11340	FInishing and Testing of Concrete chambers [Local – 03]	11	5,400.00	02-Sep-26	14-Sep-26	14-Oct-26		5,400.00	3,780.00	0.70
Local – 04		207	310,690.20	27-Jun-26	04-Oct-26	28-Jan-26		310,690.20	122,748.00	0.40
Stormwater Utilities		205	185,061.10	27-Jun-26	04-Oct-26	28-Jan-26		185,061.10	45,420.50	0.25
Pipe Work		135	45,392.50	27-Jun-26	19-Aug-26	28-Jan-26		45,392.50	34,035.50	0.75
CON-LEG101-LR-3630	Excavation for Stormwater Utilities Network [Local – 04]	7	9,079.50	27-Jun-26	04-Jul-26	28-Jan-26	29-Jan-26	9,079.50	9,079.50	1.00
CON-LEG101-LR-3730	Granular bedding for Stormwater Utilities Network [Local – 04]	4	2,263.00	05-Jul-26	08-Jul-26	31-Jan-26	31-Jan-26	2,263.00	2,263.00	1.00
CON-LEG101-LR-3830	Installation of Pipe for Stormwater Utilities Network [Local – 04]	8	20,430.00	09-Jul-26	18-Jul-26	01-Feb-26	02-Feb-26	20,430.00	20,430.00	1.00
CON-LEG101-LR-4030	Granular Surround for Stormwater Utilities Network [Local – 04]	8	2,263.00	02-Aug-26	10-Aug-26	01-Feb-26	02-Feb-26	2,263.00	2,263.00	1.00
CON-LEG101-LR-3930	Testing for Stormwater Utilities Network [Local – 04]	12	4,547.00	19-Jul-26	01-Aug-26			4,547.00	0.00	0.00
CON-LEG101-LR-4140	Installation of Micron Marker Magnetic Tape [Local – 04]	2	2,263.00	13-Aug-26	15-Aug-26			2,263.00	0.00	0.00
CON-LEG101-LR-4250	Backfilling to Subgrade Elevation [Local – 04]	4	4,547.00	16-Aug-26	19-Aug-26			4,547.00	0.00	0.00
Manhole		184	21,945.00	05-Jul-26	04-Oct-26	28-Jan-26		21,945.00	11,385.00	0.52
CON-LEG101-LR-11350	Excavation of Inlet Manholes [Local – 04]	10	3,300.00	05-Jul-26	15-Jul-26	28-Jan-26	29-Jan-26	3,300.00	3,300.00	1.00
CON-LEG101-LR-11360	PC of Inlet Manholes [Local – 04]	3	2,145.00	16-Jul-26	19-Jul-26	01-Mar-26	01-Mar-26	2,145.00	2,145.00	1.00
CON-LEG101-LR-11380	Backfilling of Inlet Manholes [Local – 04]	6	4,455.00	01-Aug-26	06-Aug-26			4,455.00	0.00	0.00
CON-LEG101-LR-11390	Finishing and Testing of Inlet Manholes [Local – 04]	15	2,145.00	16-Sep-26	04-Oct-26			2,145.00	0.00	0.00
CON-LEG101-LR-4370	Installation of Inlet Manholes [Local – 04]	10	9,900.00	20-Jul-26	30-Jul-26	07-Mar-26		9,900.00	5,940.00	0.60
Concrete Chambers/Outfalls		42	117,723.60	01-Aug-26	29-Sep-26			117,723.60	0.00	0.00
CON-LEG101-LR-11400	Excavation of Concrete chambers [Local – 04]	6	7,440.00	01-Aug-26	06-Aug-26			7,440.00	0.00	0.00
CON-LEG101-LR-11410	PC of Concrete chambers [Local – 04]	2	4,920.00	08-Aug-26	09-Aug-26			4,920.00	0.00	0.00
CON-LEG101-LR-11430	Backfilling to Concrete chambers [Local – 04]	6	10,100.00	29-Aug-26	03-Sep-26			10,100.00	0.00	0.00
CON-LEG101-LR-11420	Installation UPVC Pipes to Concrete chambers [Local – 04]	6	67,883.60	22-Aug-26	27-Aug-26			67,883.60	0.00	0.00
CON-LEG101-LR-11440	FInishing and Testing of Concrete chambers [Local – 04]	12	4,920.00	15-Sep-26	29-Sep-26			4,920.00	0.00	0.00
CON-LEG101-LR-4470	Installation of Concrete chambers [Local – 04]	10	22,460.00	10-Aug-26	20-Aug-26			22,460.00	0.00	0.00
Sanitary Sewerage		172	125,629.10	05-Jul-26	19-Aug-26	28-Jan-26		125,629.10	77,327.50	0.62
Pipe Work		172	82,749.10	05-Jul-26	19-Aug-26	28-Jan-26		82,749.10	45,167.50	0.55

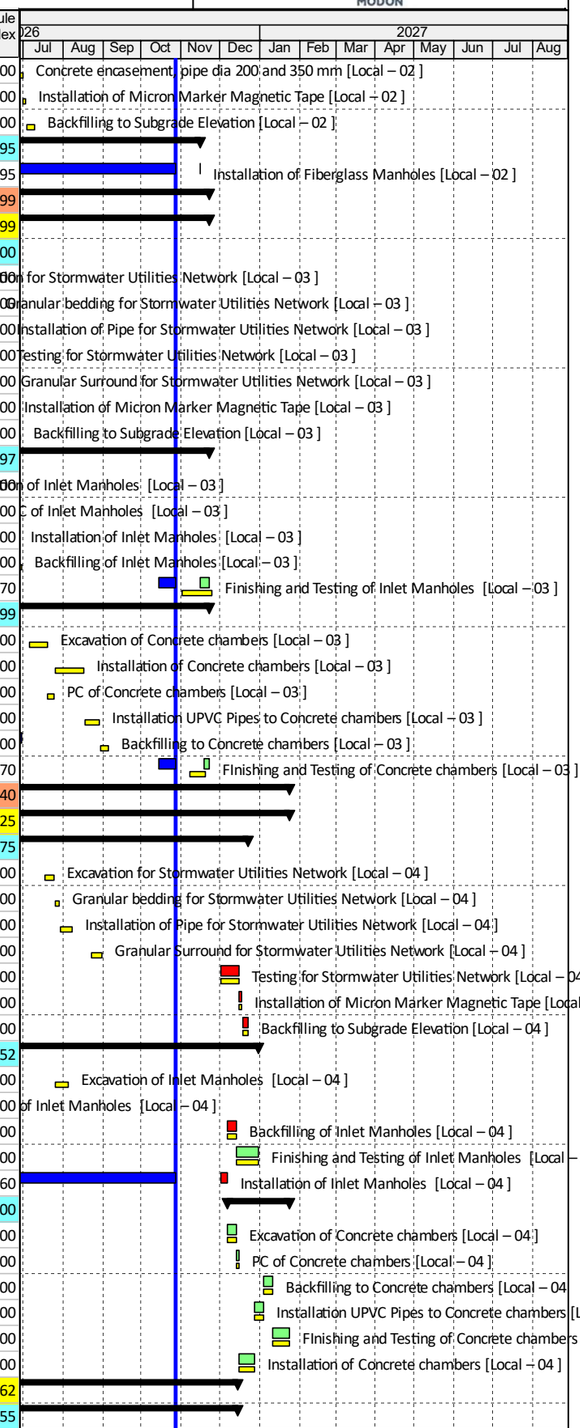


© Oracle Corporation

Activity ID	Activity Name	Original Duration	Budgeted Total Cost	BL Project Start	BL Project Finish	Actual Start	Actual Finish	Planned Value Cost	Earned Value Cost	Schedule Performance Index
CON-LEG101-LR-2820	Excavation for Sanitary Sewerage Network [Local – 04]	10	10,631.70	05-Jul-26	15-Jul-26	28-Jan-26	29-Jan-26	10,631.70	10,631.70	1.00
CON-LEG101-LR-2910	Granular bedding for Sanitary Sewerage Network [Local – 04]	2	2,620.70	16-Jul-26	18-Jul-26	30-Jan-26	31-Jan-26	2,620.70	2,620.70	1.00
CON-LEG101-LR-3000	Installation of Pipe for Sanitary Sewerage Network [Local – 04]	12	23,932.30	19-Jul-26	01-Aug-26	01-Feb-26	02-Feb-26	23,932.30	23,932.30	1.00
CON-LEG101-LR-3270	Granular Surround for Sanitary Sewerage Network [Local – 04]	2	2,664.70	09-Aug-26	10-Aug-26	01-Feb-26	02-Feb-26	2,664.70	2,664.70	1.00
CON-LEG101-LR-3090	Testing for Sanitary Sewerage Network [Local – 04]	3	5,318.10	02-Aug-26	04-Aug-26	26-Feb-26	02-Mar-26	5,318.10	5,318.10	1.00
CON-LEG101-LR-3180	Concrete encasement, pipe dia 200 and 350 mm [Local – 04]	3	29,598.80	05-Aug-26	08-Aug-26			29,598.80	0.00	0.00
CON-LEG101-LR-3360	Installation of Micron Marker Magnetic Tape [Local – 04]	2	2,664.70	11-Aug-26	12-Aug-26			2,664.70	0.00	0.00
CON-LEG101-LR-3450	Backfilling to Subgrade Elevation [Local – 04]	6	5,318.10	13-Aug-26	19-Aug-26			5,318.10	0.00	0.00
Manhole		10	42,880.00	02-Aug-26	12-Aug-26	28-Jan-26		42,880.00	32,160.00	0.75
CON-LEG101-LR-3540	Installation of Fiberglass Manholes [Local – 04]	10	42,880.00	02-Aug-26	12-Aug-26	28-Jan-26		42,880.00	32,160.00	0.75
Local – 05		129	1,252,870.00	05-Jul-26	17-Oct-26	20-Jan-26		1,252,870.00	1,246,036.00	0.99
Stormwater Utilities		126	855,697.10	05-Jul-26	17-Oct-26	21-Jan-26	24-Aug-26	855,697.10	855,697.10	1.00
Pipe Work		71	464,432.00	05-Jul-26	24-Aug-26	21-Jan-26	30-Apr-26	464,432.00	464,432.00	1.00
CON-LEG101-LR-3640	Excavation for Stormwater Utilities Network [Local – 05]	10	92,863.50	05-Jul-26	15-Jul-26	21-Jan-26	23-Apr-26	92,863.50	92,863.50	1.00
CON-LEG101-LR-3740	Granular bedding for Stormwater Utilities Network [Local – 05]	4	23,228.50	16-Jul-26	20-Jul-26	22-Jan-26	25-Apr-26	23,228.50	23,228.50	1.00
CON-LEG101-LR-3840	Installation of Pipe for Stormwater Utilities Network [Local – 05]	8	208,985.00	21-Jul-26	29-Jul-26	24-Jan-26	26-Apr-26	208,985.00	208,985.00	1.00
CON-LEG101-LR-3940	Testing for Stormwater Utilities Network [Local – 05]	6	46,443.00	30-Jul-26	05-Aug-26	11-Mar-26	28-Apr-26	46,443.00	46,443.00	1.00
CON-LEG101-LR-4040	Granular Surround for Stormwater Utilities Network [Local – 05]	6	23,228.50	06-Aug-26	12-Aug-26	25-Jan-26	28-Apr-26	23,228.50	23,228.50	1.00
CON-LEG101-LR-4150	Installation of Micron Marker Magnetic Tape [Local – 05]	2	23,228.50	13-Aug-26	15-Aug-26	14-Mar-26	29-Apr-26	23,228.50	23,228.50	1.00
CON-LEG101-LR-4260	Backfilling to Subgrade Elevation [Local – 05]	8	46,455.00	16-Aug-26	24-Aug-26	16-Mar-26	30-Apr-26	46,455.00	46,455.00	1.00
Manhole		114	113,505.00	16-Jul-26	17-Oct-26	21-Jan-26	24-Aug-26	113,505.00	113,505.00	1.00
CON-LEG101-LR-11450	Excavation of Inlet Manholes [Local – 05]	10	17,025.00	16-Jul-26	27-Jul-26	21-Jan-26	26-Apr-26	17,025.00	17,025.00	1.00
CON-LEG101-LR-11460	PC of Inlet Manholes [Local – 05]	3	11,430.00	28-Jul-26	30-Jul-26	04-Feb-26	27-Apr-26	11,430.00	11,430.00	1.00
CON-LEG101-LR-4380	Installation of Inlet Manholes [Local – 05]	10	51,000.00	01-Aug-26	11-Aug-26	11-Feb-26	30-Apr-26	51,000.00	51,000.00	1.00
CON-LEG101-LR-11470	Backfilling of Inlet Manholes [Local – 05]	8	22,620.00	12-Aug-26	20-Aug-26	15-Apr-26	07-May-26	22,620.00	22,620.00	1.00
CON-LEG101-LR-11480	Finishing and Testing of Inlet Manholes [Local – 05]	11	11,430.00	05-Oct-26	17-Oct-26	04-Jul-26	24-Aug-26	11,430.00	11,430.00	1.00
Concrete Chambers/Outfalls		99	277,760.10	12-Aug-26	15-Oct-26	02-May-26	23-Aug-26	277,760.10	277,760.10	1.00
CON-LEG101-LR-11490	Excavation of Concrete chambers [Local – 05]	6	21,100.00	12-Aug-26	18-Aug-26	02-May-26	10-May-26	21,100.00	21,100.00	1.00
CON-LEG101-LR-11500	PC of Concrete chambers [Local – 05]	2	14,040.00	19-Aug-26	20-Aug-26	03-May-26	11-May-26	14,040.00	14,040.00	1.00
CON-LEG101-LR-4480	Installation of Concrete chambers [Local – 05]	10	63,220.00	22-Aug-26	01-Sep-26	04-May-26	13-May-26	63,220.00	63,220.00	1.00
CON-LEG101-LR-11510	Installation UPVC Pipes to Concrete chambers [Local – 05]	4	137,140.10	02-Sep-26	06-Sep-26	04-May-26	14-May-26	137,140.10	137,140.10	1.00
CON-LEG101-LR-11520	Backfilling to Concrete chambers [Local – 05]	4	28,220.00	07-Sep-26	10-Sep-26	07-May-26	16-May-26	28,220.00	28,220.00	1.00
CON-LEG101-LR-11530	FInishing and Testing of Concrete chambers [Local – 05]	14	14,040.00	30-Sep-26	15-Oct-26	04-Jul-26	23-Aug-26	14,040.00	14,040.00	1.00
Sanitary Sewerage		94	397,172.90	16-Jul-26	29-Aug-26	20-Jan-26		397,172.90	390,338.90	0.98
Pipe Work		86	260,492.90	16-Jul-26	26-Aug-26	20-Jan-26	07-May-26	260,492.90	260,492.90	1.00
CON-LEG101-LR-2830	Excavation for Sanitary Sewerage Network [Local – 05]	8	44,697.00	16-Jul-26	25-Jul-26	20-Jan-26	09-Feb-26	44,697.00	44,697.00	1.00
CON-LEG101-LR-3200	Concrete encasement, pipe dia 200 and 350 mm [Local – 05]	4	36,997.40	13-Aug-26	17-Aug-26	10-Feb-26	10-Feb-26	36,997.40	36,997.40	1.00
CON-LEG101-LR-2920	Granular bedding for Sanitary Sewerage Network [Local – 05]	4	11,176.00	26-Jul-26	29-Jul-26	21-Jan-26	21-Apr-26	11,176.00	11,176.00	1.00
CON-LEG101-LR-3010	Installation of Pipe for Sanitary Sewerage Network [Local – 05]	8	100,573.50	30-Jul-26	08-Aug-26	22-Jan-26	23-Apr-26	100,573.50	100,573.50	1.00
CON-LEG101-LR-3100	Testing for Sanitary Sewerage Network [Local – 05]	4	22,348.50	09-Aug-26	12-Aug-26	01-Mar-26	03-May-26	22,348.50	22,348.50	1.00
CON-LEG101-LR-3280	Granular Surround for Sanitary Sewerage Network [Local – 05]	2	11,176.00	18-Aug-26	19-Aug-26	24-Jan-26	05-May-26	11,176.00	11,176.00	1.00
CON-LEG101-LR-3370	Installation of Micron Marker Magnetic Tape [Local – 05]	2	11,176.00	20-Aug-26	22-Aug-26	11-Mar-26	06-May-26	11,176.00	11,176.00	1.00
CON-LEG101-LR-3460	Backfilling to Subgrade Elevation [Local – 05]	4	22,348.50	23-Aug-26	26-Aug-26	14-Mar-26	07-May-26	22,348.50	22,348.50	1.00
Manhole		18	136,680.00	09-Aug-26	29-Aug-26	20-Jan-26		136,680.00	129,846.00	0.95
CON-LEG101-LR-3550	Installation of Fiberglass Manholes [Local – 05]	18	136,680.00	09-Aug-26	29-Aug-26	20-Jan-26		136,680.00	129,846.00	0.95
Local – 06		144	602,826.20	05-Jul-26	29-Oct-26	11-Feb-26	23-Aug-26	600,734.03	602,826.20	1.00
Stormwater Utilities		144	415,452.00	05-Jul-26	29-Oct-26	17-Feb-26	23-Aug-26	413,359.83	415,452.00	1.01
Pipe Work		42	181,630.00	05-Jul-26	30-Aug-26	17-Feb-26	16-May-26	181,630.00	181,630.00	1.00
CON-LEG101-LR-3650	Excavation for Stormwater Utilities Network [Local – 06]	10	36,326.00	05-Jul-26	15-Jul-26	17-Feb-26	28-Mar-26	36,326.00	36,326.00	1.00
CON-LEG101-LR-3750	Granular bedding for Stormwater Utilities Network [Local – 06]	4	9,079.50	16-Jul-26	20-Jul-26	18-Feb-26	27-Apr-26	9,079.50	9,079.50	1.00
CON-LEG101-LR-3850	Installation of Pipe for Stormwater Utilities Network [Local – 06]	10	81,731.50	21-Jul-26	01-Aug-26	19-Feb-26	29-Apr-26	81,731.50	81,731.50	1.00
CON-LEG101-LR-3950	Testing for Stormwater Utilities Network [Local – 06]	8	18,167.00	02-Aug-26	10-Aug-26	11-Apr-26	11-May-26	18,167.00	18,167.00	1.00
CON-LEG101-LR-4050	Granular Surround for Stormwater Utilities Network [Local – 06]	8	9,079.50	11-Aug-26	19-Aug-26	19-Feb-26	12-May-26	9,079.50	9,079.50	1.00

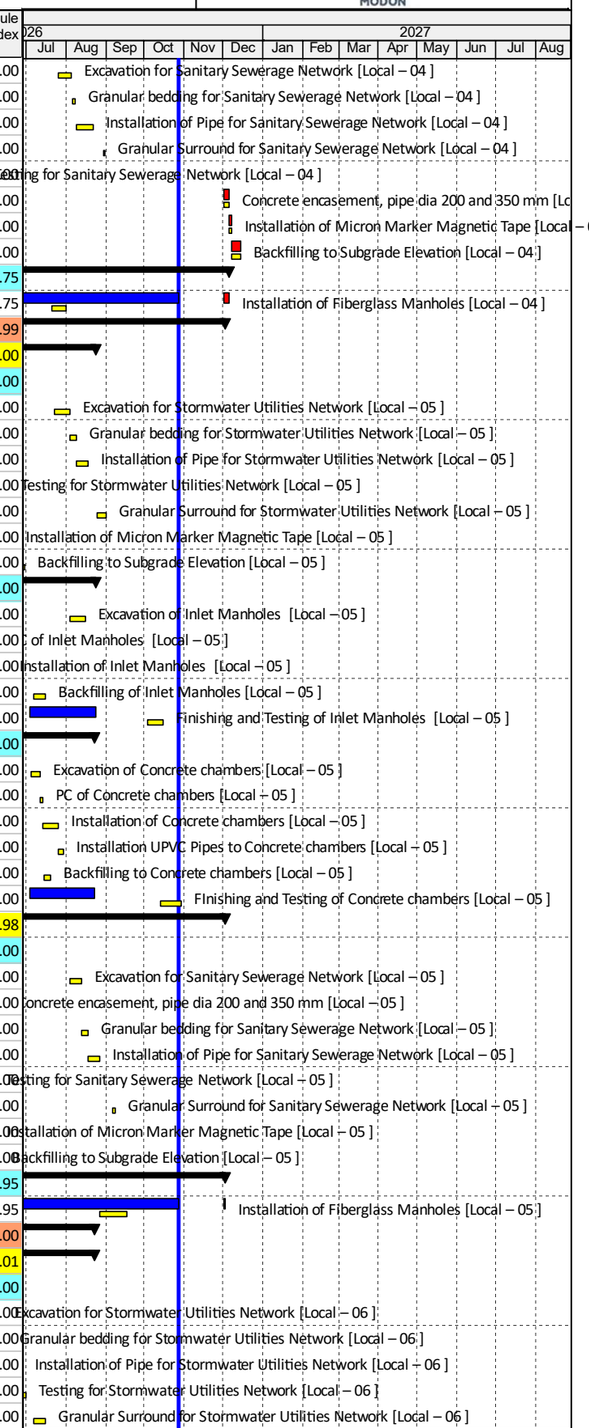


© Oracle Corporation

Activity ID	Activity Name	Original Duration	Budgeted Total Cost	BL Project Start	BL Project Finish	Actual Start	Actual Finish	Planned Value Cost	Earned Value Cost	Schedule Performance Index
CON-LEG101-LR-4160	Installation of Micron Marker Magnetic Tape [Local – 06]	2	9,079.50	20-Aug-26	22-Aug-26	20-Apr-26	13-May-26	9,079.50	9,079.50	1.00
CON-LEG101-LR-4280	Backfilling to Subgrade Elevation [Local – 06]	7	18,167.00	23-Aug-26	30-Aug-26	22-Apr-26	16-May-26	18,167.00	18,167.00	1.00
Manhole		123	77,055.00	16-Jul-26	28-Oct-26	17-Feb-26	22-Aug-26	76,279.50	77,055.00	1.01
CON-LEG101-LR-11540	Excavation of Inlet Manholes [Local – 06]	10	11,550.00	16-Jul-26	27-Jul-26	17-Feb-26	28-Mar-26	11,550.00	11,550.00	1.00
CON-LEG101-LR-11550	PC of Inlet Manholes [Local – 06]	5	7,755.00	28-Jul-26	02-Aug-26	29-Mar-26	30-Mar-26	7,755.00	7,755.00	1.00
CON-LEG101-LR-4390	Installation of Inlet Manholes [Local – 06]	10	34,650.00	03-Aug-26	13-Aug-26	01-Apr-26	03-Jun-26	34,650.00	34,650.00	1.00
CON-LEG101-LR-11560	Backfilling of Inlet Manholes [Local – 06]	8	15,345.00	15-Aug-26	23-Aug-26	22-Apr-26	06-Jun-26	15,345.00	15,345.00	1.00
CON-LEG101-LR-11570	Finishing and Testing of Inlet Manholes [Local – 06]	10	7,755.00	18-Oct-26	28-Oct-26	01-Aug-26	22-Aug-26	6,979.50	7,755.00	1.11
Concrete Chambers/Outfalls		112	156,767.00	15-Aug-26	29-Oct-26	09-May-26	23-Aug-26	155,450.33	156,767.00	1.01
CON-LEG101-LR-11580	Excavation of Concrete chambers [Local – 06]	6	11,900.00	15-Aug-26	20-Aug-26	09-May-26	10-May-26	11,900.00	11,900.00	1.00
CON-LEG101-LR-11590	PC of Concrete chambers [Local – 06]	2	7,900.00	22-Aug-26	23-Aug-26	11-May-26	11-May-26	7,900.00	7,900.00	1.00
CON-LEG101-LR-4490	Installation of Concrete chambers [Local – 06]	6	35,640.00	24-Aug-26	30-Aug-26	12-May-26	14-May-26	35,640.00	35,640.00	1.00
CON-LEG101-LR-11600	Installation UPVC Pipes to Concrete chambers [Local – 06]	4	77,587.00	31-Aug-26	03-Sep-26	13-May-26	16-May-26	77,587.00	77,587.00	1.00
CON-LEG101-LR-11610	Backfilling to Concrete chambers [Local – 06]	3	15,840.00	05-Sep-26	07-Sep-26	17-May-26	21-May-26	15,840.00	15,840.00	1.00
CON-LEG101-LR-11620	FInishing and Testing of Concrete chambers [Local – 06]	12	7,900.00	17-Oct-26	29-Oct-26	02-Aug-26	23-Aug-26	6,583.33	7,900.00	1.20
Sanitary Sewerage		42	187,374.20	16-Jul-26	30-Aug-26	11-Feb-26	23-Aug-26	187,374.20	187,374.20	1.00
Pipe Work		21	133,774.20	16-Jul-26	26-Aug-26	11-Feb-26	29-Mar-26	133,774.20	133,774.20	1.00
CON-LEG101-LR-2840	Excavation for Sanitary Sewerage Network [Local – 06]	6	17,867.00	16-Jul-26	22-Jul-26	11-Feb-26	21-Feb-26	17,867.00	17,867.00	1.00
CON-LEG101-LR-2930	Granular bedding for Sanitary Sewerage Network [Local – 06]	4	4,467.70	23-Jul-26	27-Jul-26	12-Feb-26	04-Mar-26	4,467.70	4,467.70	1.00
CON-LEG101-LR-3020	Installation of Pipe for Sanitary Sewerage Network [Local – 06]	8	40,228.30	28-Jul-26	05-Aug-26	14-Feb-26	12-Mar-26	40,228.30	40,228.30	1.00
CON-LEG101-LR-3300	Granular Surround for Sanitary Sewerage Network [Local – 06]	4	4,467.70	16-Aug-26	19-Aug-26	15-Feb-26	14-Mar-26	4,467.70	4,467.70	1.00
CON-LEG101-LR-3110	Testing for Sanitary Sewerage Network [Local – 06]	4	8,939.90	06-Aug-26	10-Aug-26	14-Mar-26	15-Mar-26	8,939.90	8,939.90	1.00
CON-LEG101-LR-3210	Concrete encasement, pipe dia 200 and 350 mm [Local – 06]	4	44,396.00	11-Aug-26	15-Aug-26	25-Mar-26	25-Mar-26	44,396.00	44,396.00	1.00
CON-LEG101-LR-3390	Installation of Micron Marker Magnetic Tape [Local – 06]	2	4,467.70	20-Aug-26	22-Aug-26	17-Mar-26	26-Mar-26	4,467.70	4,467.70	1.00
CON-LEG101-LR-3480	Backfilling to Subgrade Elevation [Local – 06]	4	8,939.90	23-Aug-26	26-Aug-26	28-Mar-26	29-Mar-26	8,939.90	8,939.90	1.00
Manhole		21	53,600.00	06-Aug-26	30-Aug-26	11-Feb-26	23-Aug-26	53,600.00	53,600.00	1.00
CON-LEG101-LR-3560	Installation of Fiberglass Manholes [Local – 06]	21	53,600.00	06-Aug-26	30-Aug-26	11-Feb-26	23-Aug-26	53,600.00	53,600.00	1.00
Local – 07		155	178,979.40	14-Jul-26	07-Nov-26	18-Feb-26	23-Aug-26	174,464.40	178,979.40	1.03
Stormwater Utilities		155	91,596.80	14-Jul-26	07-Nov-26	18-Feb-26	23-Aug-26	87,081.80	91,596.80	1.05
Pipe Work		30	27,267.50	14-Jul-26	01-Aug-26	18-Feb-26	09-Apr-26	27,267.50	27,267.50	1.00
CON-LEG101-LR-3660	Excavation for Stormwater Utilities Network [Local – 07]	3	5,449.00	14-Jul-26	16-Jul-26	18-Feb-26	21-Feb-26	5,449.00	5,449.00	1.00
CON-LEG101-LR-3760	Granular bedding for Stormwater Utilities Network [Local – 07]	2	1,367.50	18-Jul-26	19-Jul-26	22-Feb-26	22-Feb-26	1,367.50	1,367.50	1.00
CON-LEG101-LR-3860	Installation of Pipe for Stormwater Utilities Network [Local – 07]	2	12,259.00	20-Jul-26	21-Jul-26	22-Feb-26	23-Feb-26	12,259.00	12,259.00	1.00
CON-LEG101-LR-4060	Granular Surround for Stormwater Utilities Network [Local – 07]	2	1,367.50	25-Jul-26	26-Jul-26	24-Feb-26	24-Feb-26	1,367.50	1,367.50	1.00
CON-LEG101-LR-3960	Testing for Stormwater Utilities Network [Local – 07]	2	2,728.50	22-Jul-26	23-Jul-26	15-Mar-26	16-Mar-26	2,728.50	2,728.50	1.00
CON-LEG101-LR-4180	Installation of Micron Marker Magnetic Tape [Local – 07]	3	1,367.50	27-Jul-26	29-Jul-26	05-Apr-26	06-Apr-26	1,367.50	1,367.50	1.00
CON-LEG101-LR-4290	Backfilling to Subgrade Elevation [Local – 07]	2	2,728.50	30-Jul-26	01-Aug-26	08-Apr-26	09-Apr-26	2,728.50	2,728.50	1.00
Manhole		137	11,055.00	02-Aug-26	07-Nov-26	18-Feb-26	23-Aug-26	9,900.00	11,055.00	1.12
CON-LEG101-LR-11630	Excavation of Inlet Manholes [Local – 07]	3	1,650.00	02-Aug-26	04-Aug-26	18-Feb-26	21-Feb-26	1,650.00	1,650.00	1.00
CON-LEG101-LR-11640	PC of Inlet Manholes [Local – 07]	2	1,155.00	05-Aug-26	06-Aug-26	22-Feb-26	22-Feb-26	1,155.00	1,155.00	1.00
CON-LEG101-LR-4400	Installation of Inlet Manholes [Local – 07]	8	4,950.00	08-Aug-26	16-Aug-26	10-Mar-26	25-Apr-26	4,950.00	4,950.00	1.00
CON-LEG101-LR-11650	Backfilling of Inlet Manholes [Local – 07]	8	2,145.00	17-Aug-26	25-Aug-26	26-Apr-26	29-Apr-26	2,145.00	2,145.00	1.00
CON-LEG101-LR-11660	Finishing and Testing of Inlet Manholes [Local – 07]	8	1,155.00	29-Oct-26	07-Nov-26	05-Aug-26	23-Aug-26	0.00	1,155.00	0.00
Concrete Chambers/Outfalls		128	53,274.30	17-Aug-26	05-Nov-26	25-Apr-26	23-Aug-26	49,914.30	53,274.30	1.07
CON-LEG101-LR-11670	Excavation of Concrete chambers [Local – 07]	3	5,040.00	17-Aug-26	19-Aug-26	25-Apr-26	26-Apr-26	5,040.00	5,040.00	1.00
CON-LEG101-LR-11680	PC of Concrete chambers [Local – 07]	2	3,360.00	20-Aug-26	22-Aug-26	27-Apr-26	28-Apr-26	3,360.00	3,360.00	1.00
CON-LEG101-LR-11690	Installation UPVC Pipes to Concrete chambers [Local – 07]	4	19,394.30	30-Aug-26	02-Sep-26	29-Apr-26	30-Apr-26	19,394.30	19,394.30	1.00
CON-LEG101-LR-4500	Installation of Concrete chambers [Local – 07]	6	15,260.00	23-Aug-26	29-Aug-26	29-Apr-26	30-Apr-26	15,260.00	15,260.00	1.00
CON-LEG101-LR-11700	Backfilling to Concrete chambers [Local – 07]	3	6,860.00	03-Sep-26	06-Sep-26	02-May-26	04-May-26	6,860.00	6,860.00	1.00
CON-LEG101-LR-11710	FInishing and Testing of Concrete chambers [Local – 07]	6	3,360.00	31-Oct-26	05-Nov-26	06-Aug-26	23-Aug-26	0.00	3,360.00	0.00
Sanitary Sewerage		23	87,382.60	08-Aug-26	31-Aug-26	02-May-26	23-Aug-26	87,382.60	87,382.60	1.00
Pipe Work		23	63,262.60	08-Aug-26	27-Aug-26	02-May-26	08-Jun-26	63,262.60	63,262.60	1.00
CON-LEG101-LR-2850	Excavation for Sanitary Sewerage Network [Local – 07]	3	11,176.00	08-Aug-26	10-Aug-26	02-May-26	03-May-26	11,176.00	11,176.00	1.00

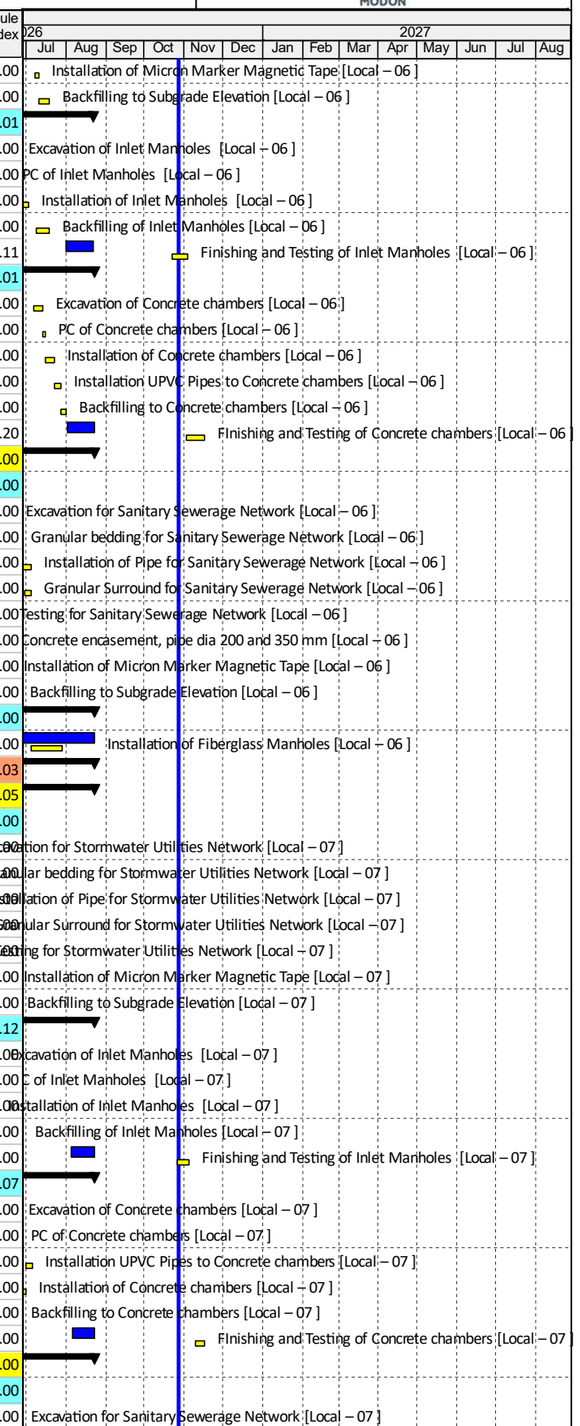


© Oracle Corporation

Activity ID	Activity Name	Original Duration	Budgeted Total Cost	BL Project Start	BL Project Finish	Actual Start	Actual Finish	Planned Value Cost	Earned Value Cost	Schedule Performance Index
CON-LEG101-LR-2940	Granular bedding for Sanitary Sewerage Network [Local – 07]	2	2,791.20	11-Aug-26	12-Aug-26	04-May-26	05-May-26	2,791.20	2,791.20	1.00
CON-LEG101-LR-3030	Installation of Pipe for Sanitary Sewerage Network [Local – 07]	4	25,143.20	13-Aug-26	17-Aug-26	06-May-26	09-May-26	25,143.20	25,143.20	1.00
CON-LEG101-LR-3120	Testing for Sanitary Sewerage Network [Local – 07]	2	5,585.60	18-Aug-26	19-Aug-26	23-May-26	24-May-26	5,585.60	5,585.60	1.00
CON-LEG101-LR-3220	Concrete encasement, pipe dia 200 and 350 mm [Local – 07]	2	7,398.60	20-Aug-26	22-Aug-26	01-Jun-26	02-Jun-26	7,398.60	7,398.60	1.00
CON-LEG101-LR-3310	Granular Surround for Sanitary Sewerage Network [Local – 07]	2	2,791.20	23-Aug-26	24-Aug-26	03-Jun-26	03-Jun-26	2,791.20	2,791.20	1.00
CON-LEG101-LR-3400	Installation of Micron Marker Magnetic Tape [Local – 07]	1	2,791.20	25-Aug-26	25-Aug-26	04-Jun-26	04-Jun-26	2,791.20	2,791.20	1.00
CON-LEG101-LR-3490	Backfilling to Subgrade Elevation [Local – 07]	2	5,585.60	26-Aug-26	27-Aug-26	06-Jun-26	08-Jun-26	5,585.60	5,585.60	1.00
Manhole		12	24,120.00	18-Aug-26	31-Aug-26	02-May-26	23-Aug-26	24,120.00	24,120.00	1.00
CON-LEG101-LR-3570	Installation of Fiberglass Manholes [Local – 07]	12	24,120.00	18-Aug-26	31-Aug-26	02-May-26	23-Aug-26	24,120.00	24,120.00	1.00
Local – 08		208	671,024.90	15-Jun-26	18-Nov-26	17-Jan-26		645,274.90	669,737.40	1.04
Stormwater Utilities		208	671,024.90	15-Jun-26	18-Nov-26	17-Jan-26		645,274.90	669,737.40	1.04
Pipe Work		83	326,932.50	15-Jun-26	10-Aug-26	17-Jan-26	07-Mar-26	326,932.50	326,932.50	1.00
CON-LEG101-LR-3670	Excavation for Stormwater Utilities Network [Local – 08]	10	65,384.50	15-Jun-26	25-Jun-26	17-Jan-26	21-Jan-26	65,384.50	65,384.50	1.00
CON-LEG101-LR-3770	Granular bedding for Stormwater Utilities Network [Local – 08]	4	16,347.00	27-Jun-26	30-Jun-26	19-Jan-26	25-Jan-26	16,347.00	16,347.00	1.00
CON-LEG101-LR-3870	Installation of Pipe for Stormwater Utilities Network [Local – 08]	10	147,116.00	01-Jul-26	12-Jul-26	20-Jan-26	31-Jan-26	147,116.00	147,116.00	1.00
CON-LEG101-LR-4080	Granular Surround for Stormwater Utilities Network [Local – 08]	6	16,347.00	22-Jul-26	28-Jul-26	20-Jan-26	01-Feb-26	16,347.00	16,347.00	1.00
CON-LEG101-LR-3970	Testing for Stormwater Utilities Network [Local – 08]	8	32,695.50	13-Jul-26	21-Jul-26	21-Feb-26	26-Feb-26	32,695.50	32,695.50	1.00
CON-LEG101-LR-4190	Installation of Micron Marker Magnetic Tape [Local – 08]	4	16,347.00	29-Jul-26	02-Aug-26	28-Feb-26	05-Mar-26	16,347.00	16,347.00	1.00
CON-LEG101-LR-4300	Backfilling to Subgrade Elevation [Local – 08]	7	32,695.50	03-Aug-26	10-Aug-26	28-Feb-26	07-Mar-26	32,695.50	32,695.50	1.00
Manhole		185	143,850.00	27-Jun-26	18-Nov-26	17-Jan-26		129,400.00	143,127.50	1.11
CON-LEG101-LR-11720	Excavation of Inlet Manholes [Local – 08]	10	21,600.00	27-Jun-26	07-Jul-26	17-Jan-26	21-Jan-26	21,600.00	21,600.00	1.00
CON-LEG101-LR-11730	PC of Inlet Manholes [Local – 08]	3	14,450.00	08-Jul-26	11-Jul-26	25-Jan-26	31-Jan-26	14,450.00	14,450.00	1.00
CON-LEG101-LR-4410	Installation of Inlet Manholes [Local – 08]	14	64,700.00	13-Jul-26	28-Jul-26	29-Jan-26	01-Jun-26	64,700.00	64,700.00	1.00
CON-LEG101-LR-11740	Backfilling of Inlet Manholes [Local – 08]	10	28,650.00	29-Jul-26	09-Aug-26	25-Mar-26	04-Jun-26	28,650.00	28,650.00	1.00
CON-LEG101-LR-11750	Finishing and Testing of Inlet Manholes [Local – 08]	10	14,450.00	08-Nov-26	18-Nov-26	26-Aug-26		0.00	13,727.50	0.00
Concrete Chambers/Outfalls		123	200,242.40	29-Jul-26	18-Nov-26	09-Jun-26		188,942.40	199,677.40	1.06
CON-LEG101-LR-11760	Excavation of Concrete chambers [Local – 08]	6	16,940.00	29-Jul-26	04-Aug-26	09-Jun-26	24-Jun-26	16,940.00	16,940.00	1.00
CON-LEG101-LR-11770	PC of Concrete chambers [Local – 08]	2	11,300.00	05-Aug-26	06-Aug-26	11-Jun-26	25-Jun-26	11,300.00	11,300.00	1.00
CON-LEG101-LR-4510	Installation of Concrete chambers [Local – 08]	12	50,760.00	08-Aug-26	20-Aug-26	13-Jun-26	27-Jun-26	50,760.00	50,760.00	1.00
CON-LEG101-LR-11780	Installation UPVC Pipes to Concrete chambers [Local – 08]	10	87,282.40	22-Aug-26	01-Sep-26	13-Jun-26	28-Jun-26	87,282.40	87,282.40	1.00
CON-LEG101-LR-11790	Backfilling to Concrete chambers [Local – 08]	6	22,660.00	02-Sep-26	08-Sep-26	17-Jun-26	30-Jun-26	22,660.00	22,660.00	1.00
CON-LEG101-LR-11800	FInishing and Testing of Concrete chambers [Local – 08]	11	11,300.00	07-Nov-26	18-Nov-26	26-Aug-26		0.00	10,735.00	0.00
Shallow infrastructure network		439	12,539,076.30	15-Jun-26	18-Mar-27	13-Jan-26		3,274,728.64	10,520,647.69	3.21
Local – 01		373	5,253,105.10	15-Jun-26	18-Mar-27	13-Jan-26		1,572,304.65	4,904,663.44	3.12
LOCAL - 01 Segment-01 (From 0+000 to 1+066)		373	2,096,465.90	16-Jun-26	18-Mar-27	13-Jan-26		641,631.56	1,884,644.63	2.94
TSE Network		232	424,147.50	16-Jun-26	21-Dec-26	13-Jan-26	05-Sep-26	327,801.50	424,147.50	1.29
Pipe Work		159	223,147.50	16-Jun-26	08-Oct-26	13-Jan-26	04-May-26	223,147.50	223,147.50	1.00
CON-LEG101-LR-1300	Excavation for TSE Network [Local – 01 Segment-01]	15	44,285.50	16-Jun-26	02-Jul-26	13-Jan-26	21-Jan-26	44,285.50	44,285.50	1.00
CON-LEG101-LR-1410	Granular bedding for TSE Network [Local – 01 Segment-01]	12	11,079.20	04-Jul-26	16-Jul-26	14-Jan-26	22-Jan-26	11,079.20	11,079.20	1.00
CON-LEG101-LR-1520	Installation of Pipe for TSE Network [Local – 01 Segment-01]	20	99,710.20	18-Jul-26	09-Aug-26	15-Jan-26	19-Feb-26	99,710.20	99,710.20	1.00
CON-LEG101-LR-1850	Granular Surround for TSE Network [Local – 01 Segment-01]	14	11,079.20	30-Aug-26	14-Sep-26	25-Jan-26	19-Feb-26	11,079.20	11,079.20	1.00
CON-LEG101-LR-1960	Installation of Micron Marker Magnetic Tape [Local – 01 Segment-01]	6	11,079.20	15-Sep-26	21-Sep-26	07-Feb-26	21-Feb-26	11,079.20	11,079.20	1.00
CON-LEG101-LR-2070	Backfilling to Subgrade Elevation [Local – 01 Segment-01]	14	22,159.10	22-Sep-26	08-Oct-26	08-Feb-26	23-Feb-26	22,159.10	22,159.10	1.00
CON-LEG101-LR-1750	Concrete encasement, pipe dia 110 mm [Local – 01 Segment-01]	3	1,596.00	26-Aug-26	29-Aug-26	28-Feb-26	01-Mar-26	1,596.00	1,596.00	1.00
CON-LEG101-LR-1640	Testing for TSE Network [Local – 01 Segment-01]	14	22,159.10	10-Aug-26	25-Aug-26	10-Mar-26	04-May-26	22,159.10	22,159.10	1.00
Valves/Chamber		215	201,000.00	10-Aug-26	21-Dec-26	25-Feb-26	05-Sep-26	104,654.00	201,000.00	1.92
CON-LEG101-LR-2460	Installation of Fire Hydrant [Local – 01 Segment-01]	21	84,420.00	28-Nov-26	21-Dec-26	25-Feb-26	01-Jul-26	0.00	84,420.00	0.00
CON-LEG101-LR-2190	Installation of Gate (Sluice) valves (Direct buried) [Local – 01 Segment-(	21	48,910.00	29-Sep-26	22-Oct-26	28-Feb-26	02-Jul-26	48,910.00	48,910.00	1.00
CON-LEG101-LR-2310	Installation of Wash-out Valves [Local – 01 Segment-01]	15	8,040.00	24-Oct-26	09-Nov-26	28-Feb-26	02-Jul-26	2,144.00	8,040.00	3.75
CON-LEG101-LR-2380	Installation of Air Valves [Local – 01 Segment-01]	15	6,030.00	10-Nov-26	26-Nov-26	28-Feb-26	02-Jul-26	0.00	6,030.00	0.00
CON-LEG101-LR-2610	Installation of Wash out chambers [Local – 01 Segment-01]	21	26,800.00	10-Aug-26	02-Sep-26	21-Apr-26	03-Sep-26	26,800.00	26,800.00	1.00
CON-LEG101-LR-2680	Installation of Air Valve chambers [Local – 01 Segment-01]	21	26,800.00	03-Sep-26	28-Sep-26	28-Feb-26	05-Sep-26	26,800.00	26,800.00	1.00
Public Water Utility Distribution		99	315,189.20	04-Jul-26	05-Nov-26	13-Jan-26	05-Sep-26	306,862.06	315,189.20	1.03

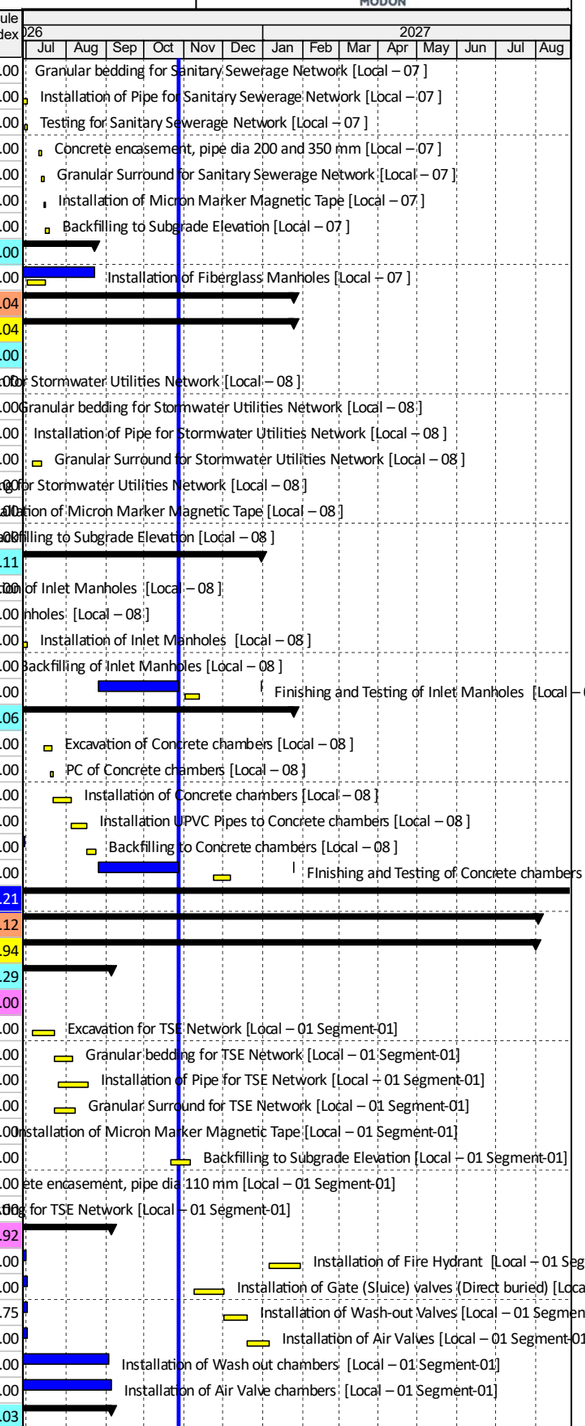


© Oracle Corporation

Activity ID	Activity Name	Original Duration	Budgeted Total Cost	BL Project Start	BL Project Finish	Actual Start	Actual Finish	Planned Value Cost	Earned Value Cost	Schedule Performance Index
Pipe Work		99	189,229.20	04-Jul-26	08-Oct-26	13-Jan-26	24-Mar-26	189,229.20	189,229.20	1.00
CON-LEG101-LR-10040	Excavation for Public Water Utility Distribution Piping [Local – 01 Segm	17	37,852.80	04-Jul-26	22-Jul-26	13-Jan-26	21-Jan-26	37,852.80	37,852.80	1.00
CON-LEG101-LR-10140	Granular bedding for Public Water Utility Distribution Piping [Local – 01	10	9,448.50	23-Jul-26	03-Aug-26	13-Jan-26	22-Jan-26	9,448.50	9,448.50	1.00
CON-LEG101-LR-10540	Granular Surround for Public Water Utility Distribution Piping [Local – 0	13	9,462.00	09-Sep-26	24-Sep-26	26-Jan-26	19-Feb-26	9,462.00	9,462.00	1.00
CON-LEG101-LR-10240	Installation of Pipe for Public Water Utility Distribution Piping [Local – 0	18	85,157.70	04-Aug-26	24-Aug-26	15-Jan-26	19-Feb-26	85,157.70	85,157.70	1.00
CON-LEG101-LR-10640	Installation of Micron Marker Magnetic Tape [Local – 01 Segment-01]	2	9,462.00	26-Sep-26	27-Sep-26	07-Feb-26	21-Feb-26	9,462.00	9,462.00	1.00
CON-LEG101-LR-10740	Backfilling to Subgrade Elevation [Local – 01 Segment-01]	10	18,923.10	28-Sep-26	08-Oct-26	08-Feb-26	23-Feb-26	18,923.10	18,923.10	1.00
CON-LEG101-LR-10440	Concrete encasement, pipe dia 110 mm [Local – 01 Segment-01]	3	0.00	06-Sep-26	08-Sep-26	28-Feb-26	01-Mar-26	0.00	0.00	0.00
CON-LEG101-LR-10340	Testing for Public Water Utility Distribution Piping [Local – 01 Segment-	10	18,923.10	25-Aug-26	05-Sep-26	11-Mar-26	24-Mar-26	18,923.10	18,923.10	1.00
Valves/Chamber		55	125,960.00	03-Sep-26	05-Nov-26	28-Feb-26	05-Sep-26	117,632.86	125,960.00	1.07
CON-LEG101-LR-1110	Installation of Wash-out Valves [Local – 01 Segment-01]	7	16,080.00	21-Oct-26	28-Oct-26	28-Feb-26	02-Jul-26	13,782.86	16,080.00	1.17
CON-LEG101-LR-1150	Installation of Air Valves [Local – 01 Segment-01]	7	6,030.00	29-Oct-26	05-Nov-26	28-Feb-26	02-Jul-26	0.00	6,030.00	0.00
CON-LEG101-LR-1000	Installation of Gate (Sluice) valves (Direct buried) [Local – 01 Segment-(	10	23,450.00	10-Oct-26	20-Oct-26	28-Feb-26	05-Aug-26	23,450.00	23,450.00	1.00
CON-LEG101-LR-1210	Installation of Wash out chambers [Local – 01 Segment-01]	20	53,600.00	03-Sep-26	27-Sep-26	21-Apr-26	03-Sep-26	53,600.00	53,600.00	1.00
CON-LEG101-LR-1250	Installation of Air Valve chambers [Local – 01 Segment-01]	20	26,800.00	28-Sep-26	20-Oct-26	28-Feb-26	05-Sep-26	26,800.00	26,800.00	1.00
Electrical Works		105	174,565.00	10-Oct-26	15-Feb-27	02-Apr-26		0.00	142,843.30	0.00
Low Voltage		105	174,565.00	10-Oct-26	15-Feb-27	02-Apr-26		0.00	142,843.30	0.00
CON-LEG101-LR-7980	Installation of Low Voltage Cables Duct Banks [Local – 01 Segment-01]	12	16,961.50	29-Oct-26	11-Nov-26	02-Apr-26	30-Apr-26	0.00	16,961.50	0.00
CON-LEG101-LR-7780	Excavation works for Low Voltage Cables [Local – 01 Segment-01]	17	0.00	10-Oct-26	28-Oct-26	01-Jun-26		0.00	0.00	0.00
CON-LEG101-LR-7880	Installation of Low Voltage Cables [Local – 01 Segment-01]	21	155,593.50	12-Nov-26	06-Dec-26	04-Jun-26		0.00	124,474.80	0.00
CON-LEG101-LR-8760	Installation of Earthing System [Local – 01 Segment-01]	7	2,010.00	03-Feb-27	15-Feb-27	05-Jul-26		0.00	1,407.00	0.00
Telecommunications		123	359,401.95	29-Oct-26	14-Mar-27	02-Apr-26		0.00	329,261.88	0.00
CON-LEG101-LR-8930	Installation of Concrete encased duct banks for primary network [Local	11	55,411.75	07-Dec-26	19-Dec-26	07-Apr-26	26-Apr-26	0.00	55,411.75	0.00
CON-LEG101-LR-8830	Installation of Sand and soil encased duct banks for primary network [L	20	121,846.70	29-Oct-26	21-Nov-26	02-Apr-26	30-Apr-26	0.00	121,846.70	0.00
CON-LEG101-LR-9030	Installation of Sand encased duct banks for secondary network [Local –	14	25,969.00	20-Dec-26	04-Jan-27	08-Jul-26		0.00	14,282.95	0.00
CON-LEG101-LR-9130	Installation of Sand and soil encased duct banks, for combined network	18	6,216.50	05-Jan-27	25-Jan-27	08-Jul-26		0.00	3,419.08	0.00
CON-LEG101-LR-9230	Installation of Concrete encased duct banks for for combined network (	15	1,888.00	26-Jan-27	16-Feb-27	08-Jul-26		0.00	1,038.40	0.00
CON-LEG101-LR-9330	Installation of Reinforced concrete manhole [Local – 01 Segment-01]	21	148,070.00	17-Feb-27	14-Mar-27	04-Apr-26		0.00	133,263.00	0.00
CCTV feeding system and GSM		136	622,966.25	22-Nov-26	18-Mar-27	13-Apr-26		0.00	477,696.75	0.00
CON-LEG101-LR-9870	Installation of 35 Meters mono pole with Double Platform for Access Pc	2	107,200.00	17-Mar-27	18-Mar-27	16-May-26	08-Jul-26	0.00	107,200.00	0.00
CON-LEG101-LR-9880	Installation of 25 Meters pole for CCTV Cameras [Local – 01 Segment-0	2	174,200.00	17-Mar-27	18-Mar-27	16-May-26	12-Jul-26	0.00	174,200.00	0.00
CON-LEG101-LR-8550	Excavation works for Low Voltage Cables for CCTV feeding system and (	6	4,020.00	22-Nov-26	28-Nov-26	13-Apr-26		0.00	3,618.00	0.00
CON-LEG101-LR-8620	Installation of Low Voltage Cables for CCTV feeding system and GSM [L	4	18,626.25	29-Nov-26	02-Dec-26	29-Aug-26		0.00	11,175.75	0.00
CON-LEG101-LR-9430	Installation of Fiber Optic Patch Panel 12 port [Local – 01 Segment-01]	7	6,700.00	03-Dec-26	10-Dec-26	01-Jul-26		0.00	6,030.00	0.00
CON-LEG101-LR-9450	Installation of Modular Industrial Switches for main pole [Local – 01 Seg	7	10,050.00	19-Dec-26	26-Dec-26	01-Jul-26		0.00	9,045.00	0.00
CON-LEG101-LR-9460	Installation of 8POE ports Industrial Switches for remote poles [Local –	7	20,100.00	27-Dec-26	03-Jan-27	01-Jul-26		0.00	18,090.00	0.00
CON-LEG101-LR-9520	Installation of Core Switch [Local – 01 Segment-01]	3	20,100.00	17-Jan-27	19-Jan-27	01-Jul-26		0.00	18,090.00	0.00
CON-LEG101-LR-9540	Installation of Access Switch 48 port [Local – 01 Segment-01]	3	10,050.00	21-Jan-27	24-Jan-27	01-Jul-26		0.00	9,045.00	0.00
CON-LEG101-LR-9560	Installation of Server [Local – 01 Segment-01]	3	87,100.00	25-Jan-27	27-Jan-27	01-Jul-26		0.00	78,390.00	0.00
CON-LEG101-LR-9590	Installation of Stand rack 42U- 19" [Local – 01 Segment-01]	3	10,050.00	31-Jan-27	02-Feb-27	01-Jul-26		0.00	9,045.00	0.00
CON-LEG101-LR-9610	Installation of IP Outdoor CCTV POE Camera,5 MP, Metal Housing [Loca	3	13,400.00	03-Feb-27	06-Feb-27	01-Jul-26		0.00	12,060.00	0.00
CON-LEG101-LR-9690	Installation of Outdoor PTZ IP66 [Local – 01 Segment-01]	2	0.00	07-Feb-27	08-Feb-27	01-Jul-26		0.00	0.00	0.00
CON-LEG101-LR-9780	Installation of Security workstation with 1 x 19" LED screen [Local – 01	1	16,750.00	14-Feb-27	14-Feb-27			0.00	0.00	0.00
CON-LEG101-LR-9790	Installation of LED Screen 43" (24/7 operation) with Ethernet decoders	2	0.00	15-Feb-27	16-Feb-27			0.00	0.00	0.00
CON-LEG101-LR-9830	Installation of Network Video Recorder 4k 64 Channel [Local – 01 Segm	1	33,500.00	27-Feb-27	27-Feb-27			0.00	0.00	0.00
CON-LEG101-LR-9840	Installation of Keypad [Local – 01 Segment-01]	2	67,000.00	13-Mar-27	14-Mar-27			0.00	0.00	0.00
CON-LEG101-LR-9850	Installation of Horizontal Power Distribution Unit (min 8 outlets) [Local	2	6,700.00	15-Mar-27	16-Mar-27	01-Jul-26		0.00	6,030.00	0.00
CON-LEG101-LR-9940	Installation of Short Range wireless point to point wireless bridge [Loca	2	17,420.00	17-Mar-27	18-Mar-27	01-Jul-26		0.00	15,678.00	0.00
Earthing System		2	0.00	17-Mar-27	18-Mar-27			0.00	0.00	0.00
CON-LEG101-LR-8280	Installation of Earthing for Distribution panels,SL feeder pillars, KWH, U	2	0.00	17-Mar-27	18-Mar-27			0.00	0.00	0.00
Road Lighting		181	200,196.00	27-Oct-26	30-Dec-26	14-Mar-26		6,968.00	195,506.00	28.06
CON-LEG101-LR-8080	Installation of Lighting poles [Local – 01 Segment-01]	17	118,456.00	27-Oct-26	15-Nov-26	14-Mar-26	22-Oct-26	6,968.00	118,456.00	17.00
CON-LEG101-LR-8180	Installation of Street Lighting Luminaire [Local – 01 Segment-01]	12	34,840.00	16-Nov-26	29-Nov-26	16-May-26	22-Oct-26	0.00	34,840.00	0.00

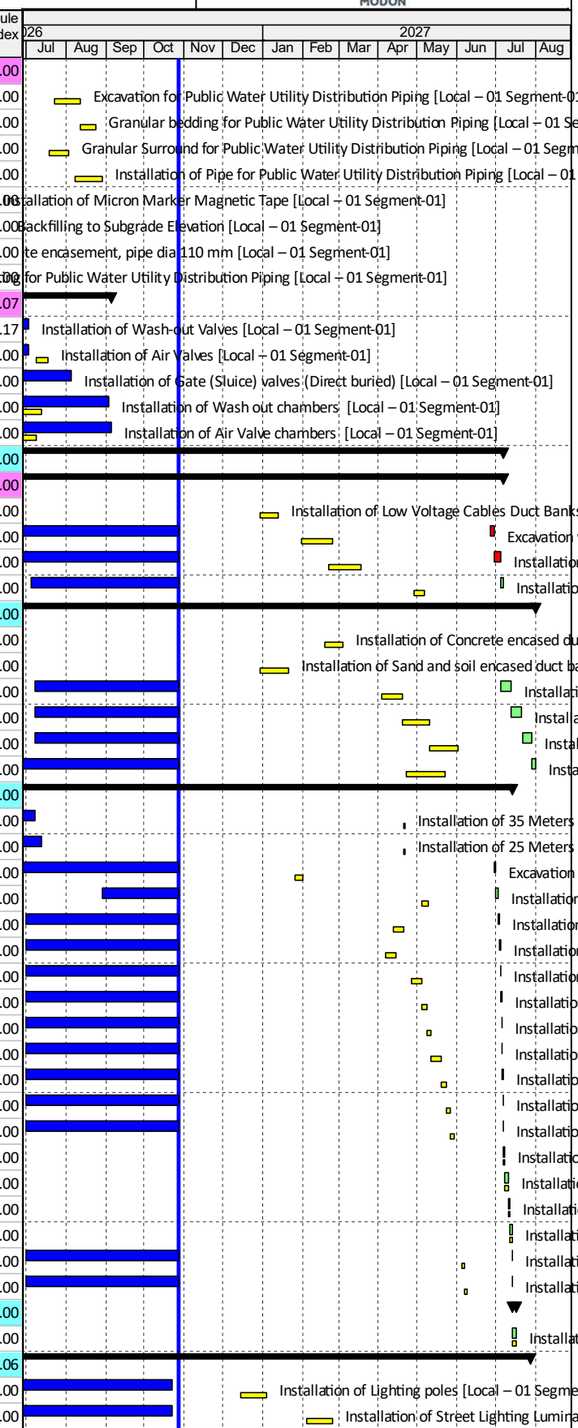


© Oracle Corporation

Activity ID	Activity Name	Original Duration	Budgeted Total Cost	BL Project Start	BL Project Finish	Actual Start	Actual Finish	Planned Value Cost	Earned Value Cost	Schedule Performance Index
CON-LEG101-LR-7420	Installation of Unit Substation Including concrete foundations and fencir	7	0.00	29-Nov-26	06-Dec-26	05-Jul-26		0.00	0.00	0.00
CON-LEG101-LR-7500	Installation of Ring Main Unit RMU [Local – 01 Segment-01]	15	0.00	07-Dec-26	23-Dec-26			0.00	0.00	0.00
CON-LEG101-LR-8330	Installation of Earthing for Streetlighting feeders for every end pole circ	6	0.00	24-Dec-26	30-Dec-26	01-Aug-26		0.00	0.00	0.00
CON-LEG101-LR-8430	Installation of Street Lighting feeder pillars / Lighting panels [Local – 0	3	46,900.00	30-Nov-26	02-Dec-26	05-Jul-26		0.00	42,210.00	0.00
LOCAL - 01 Segment-02 (From 1+066 to 2+133)		300	1,553,888.90	15-Jun-26	06-Mar-27	22-Jan-26		515,446.37	1,553,788.40	3.01
TSE Network		211	423,141.40	15-Jun-26	07-Jan-27	22-Jan-26	06-Sep-26	279,155.21	423,141.40	1.52
Pipe Work		87	226,831.40	15-Jun-26	26-Sep-26	22-Jan-26	02-Jun-26	226,831.40	226,831.40	1.00
CON-LEG101-LR-1310	Excavation for TSE Network [Local – 01 Segment-02]	10	44,723.50	15-Jun-26	25-Jun-26	22-Jan-26	31-Jan-26	44,723.50	44,723.50	1.00
CON-LEG101-LR-1420	Granular bedding for TSE Network [Local – 01 Segment-02]	7	11,186.40	27-Jun-26	04-Jul-26	26-Jan-26	21-May-26	11,186.40	11,186.40	1.00
CON-LEG101-LR-1530	Installation of Pipe for TSE Network [Local – 01 Segment-02]	20	100,650.90	05-Jul-26	27-Jul-26	27-Jan-26	24-May-26	100,650.90	100,650.90	1.00
CON-LEG101-LR-1760	Concrete encasement, pipe dia 110 mm [Local – 01 Segment-02]	3	3,171.00	13-Aug-26	16-Aug-26	07-Feb-26	25-May-26	3,171.00	3,171.00	1.00
CON-LEG101-LR-1860	Granular Surround for TSE Network [Local – 01 Segment-02]	14	11,186.40	17-Aug-26	01-Sep-26	29-Jan-26	25-May-26	11,186.40	11,186.40	1.00
CON-LEG101-LR-1970	Installation of Micron Marker Magnetic Tape [Local – 01 Segment-02]	6	11,186.40	02-Sep-26	08-Sep-26	25-Feb-26	31-May-26	11,186.40	11,186.40	1.00
CON-LEG101-LR-2090	Backfilling to Subgrade Elevation [Local – 01 Segment-02]	14	22,363.40	09-Sep-26	26-Sep-26	26-Feb-26	01-Jun-26	22,363.40	22,363.40	1.00
CON-LEG101-LR-1650	Testing for TSE Network [Local – 01 Segment-02]	14	22,363.40	28-Jul-26	12-Aug-26	10-Mar-26	02-Jun-26	22,363.40	22,363.40	1.00
Valves/Chamber		201	196,310.00	09-Sep-26	07-Jan-27	04-Mar-26	06-Sep-26	52,323.81	196,310.00	3.75
CON-LEG101-LR-2200	Installation of Gate (Sluice) valves (Direct buried) [Local – 01 Segment-(	10	44,220.00	07-Nov-26	17-Nov-26	04-Mar-26	08-Jul-26	0.00	44,220.00	0.00
CON-LEG101-LR-2320	Installation of Wash-out Valves [Local – 01 Segment-02]	19	8,040.00	18-Nov-26	09-Dec-26	16-Mar-26	08-Jul-26	0.00	8,040.00	0.00
CON-LEG101-LR-2390	Installation of Air Valves [Local – 01 Segment-02]	15	6,030.00	10-Dec-26	27-Dec-26	16-Mar-26	08-Jul-26	0.00	6,030.00	0.00
CON-LEG101-LR-2620	Installation of Wash out chambers [Local – 01 Segment-02]	21	26,800.00	09-Sep-26	04-Oct-26	21-Apr-26	03-Sep-26	26,800.00	26,800.00	1.00
CON-LEG101-LR-2690	Installation of Air Valve chambers [Local – 01 Segment-02]	21	26,800.00	05-Oct-26	28-Oct-26	15-Mar-26	05-Sep-26	25,523.81	26,800.00	1.05
CON-LEG101-LR-2470	Installation of Fire Hydrant [Local – 01 Segment-02]	10	84,420.00	28-Dec-26	07-Jan-27	04-Mar-26	06-Sep-26	0.00	84,420.00	0.00
Public Water Utility Distribution		157	319,690.20	15-Jun-26	06-Mar-27	22-Jan-26	05-Sep-26	193,730.20	319,690.20	1.65
Pipe Work		89	193,730.20	15-Jun-26	01-Oct-26	22-Jan-26	02-Jun-26	193,730.20	193,730.20	1.00
CON-LEG101-LR-10050	Excavation for Public Water Utility Distribution Piping [Local – 01 Segme	17	37,852.80	15-Jun-26	04-Jul-26	22-Jan-26	05-Feb-26	37,852.80	37,852.80	1.00
CON-LEG101-LR-10150	Granular bedding for Public Water Utility Distribution Piping [Local – 01	13	9,448.50	05-Jul-26	19-Jul-26	26-Jan-26	21-May-26	9,448.50	9,448.50	1.00
CON-LEG101-LR-10250	Installation of Pipe for Public Water Utility Distribution Piping [Local – 0	18	85,157.70	20-Jul-26	09-Aug-26	27-Jan-26	24-May-26	85,157.70	85,157.70	1.00
CON-LEG101-LR-10550	Granular Surround for Public Water Utility Distribution Piping [Local – 0	13	9,462.00	02-Sep-26	16-Sep-26	01-Feb-26	25-May-26	9,462.00	9,462.00	1.00
CON-LEG101-LR-10450	Concrete encasement, pipe dia 110 mm [Local – 01 Segment-02]	7	4,501.00	25-Aug-26	01-Sep-26	15-Mar-26	25-May-26	4,501.00	4,501.00	1.00
CON-LEG101-LR-10650	Installation of Micron Marker Magnetic Tape [Local – 01 Segment-02]	2	9,462.00	17-Sep-26	19-Sep-26	25-Feb-26	31-May-26	9,462.00	9,462.00	1.00
CON-LEG101-LR-10750	Backfilling to Subgrade Elevation [Local – 01 Segment-02]	10	18,923.10	20-Sep-26	01-Oct-26	26-Feb-26	01-Jun-26	18,923.10	18,923.10	1.00
CON-LEG101-LR-10350	Testing for Public Water Utility Distribution Piping [Local – 01 Segment-	13	18,923.10	10-Aug-26	24-Aug-26	17-Mar-26	02-Jun-26	18,923.10	18,923.10	1.00
Valves/Chamber		120	125,960.00	29-Oct-26	06-Mar-27	15-Mar-26	05-Sep-26	0.00	125,960.00	0.00
CON-LEG101-LR-1010	Installation of Gate (Sluice) valves (Direct buried) [Local – 01 Segment-(	21	23,450.00	17-Dec-26	10-Jan-27	29-Apr-26	08-Jul-26	0.00	23,450.00	0.00
CON-LEG101-LR-1120	Installation of Wash-out Valves [Local – 01 Segment-02]	21	16,080.00	11-Jan-27	03-Feb-27	01-Apr-26	08-Jul-26	0.00	16,080.00	0.00
CON-LEG101-LR-1160	Installation of Air Valves [Local – 01 Segment-02]	21	6,030.00	04-Feb-27	06-Mar-27	01-Apr-26	08-Jul-26	0.00	6,030.00	0.00
CON-LEG101-LR-1220	Installation of Wash out chambers [Local – 01 Segment-02]	21	53,600.00	29-Oct-26	22-Nov-26	21-Apr-26	03-Sep-26	0.00	53,600.00	0.00
CON-LEG101-LR-1260	Installation of Air Valve chambers [Local – 01 Segment-02]	21	26,800.00	23-Nov-26	16-Dec-26	15-Mar-26	05-Sep-26	0.00	26,800.00	0.00
Electrical Works		184	174,543.10	03-Oct-26	16-Feb-27	04-Apr-26		12,099.29	174,442.60	14.42
Low Voltage		184	174,543.10	03-Oct-26	16-Feb-27	04-Apr-26		12,099.29	174,442.60	14.42
CON-LEG101-LR-7990	Installation of Low Voltage Cables Duct Banks [Local – 01 Segment-02]	7	16,939.00	22-Oct-26	29-Oct-26	04-Apr-26	30-Apr-26	12,099.29	16,939.00	1.40
CON-LEG101-LR-7790	Excavation works for Low Voltage Cables [Local – 01 Segment-02]	17	0.00	03-Oct-26	21-Oct-26	24-Jun-26	30-Jul-26	0.00	0.00	0.00
CON-LEG101-LR-7890	Installation of Low Voltage Cables [Local – 01 Segment-02]	17	155,594.10	31-Oct-26	18-Nov-26	25-Jun-26	01-Aug-26	0.00	155,594.10	0.00
CON-LEG101-LR-8770	Installation of Earthing System [Local – 01 Segment-02]	8	2,010.00	03-Feb-27	16-Feb-27	06-Jul-26		0.00	1,909.50	0.00
Telecommunications		179	359,401.95	22-Oct-26	07-Feb-27	04-Apr-26	10-Sep-26	30,461.68	359,401.95	11.80
CON-LEG101-LR-8840	Installation of Sand and soil encased duct banks for primary network [L	20	121,846.70	22-Oct-26	14-Nov-26	04-Apr-26	30-Apr-26	30,461.68	121,846.70	4.00
CON-LEG101-LR-8940	Installation of Concrete encased duct banks for primary network [Local	11	55,411.75	15-Nov-26	26-Nov-26	08-Apr-26	30-Apr-26	0.00	55,411.75	0.00
CON-LEG101-LR-9040	Installation of Sand encased duct banks for secondary network [Local –	14	25,969.00	28-Nov-26	13-Dec-26	11-Jul-26	10-Sep-26	0.00	25,969.00	0.00
CON-LEG101-LR-9140	Installation of Sand and soil encased duct banks, for combined network	18	6,216.50	14-Dec-26	03-Jan-27	11-Jul-26	10-Sep-26	0.00	6,216.50	0.00
CON-LEG101-LR-9240	Installation of Concrete encased duct banks for for combined network (	9	1,888.00	04-Jan-27	13-Jan-27	11-Jul-26	10-Sep-26	0.00	1,888.00	0.00
CON-LEG101-LR-9340	Installation of Reinforced concrete manhole [Local – 01 Segment-02]	21	148,070.00	14-Jan-27	07-Feb-27	09-Apr-26	10-Sep-26	0.00	148,070.00	0.00
CCTV feeding system and GSM		26	76,916.25	04-Jan-27	07-Feb-27	04-Jul-26	07-Sep-26	0.00	76,916.25	0.00
CON-LEG101-LR-9620	Installation of IP Outdoor CCTV POE Camera,5 MP, Metal Housing [Loca	5	13,400.00	23-Jan-27	27-Jan-27	08-Jul-26	03-Sep-26	0.00	13,400.00	0.00

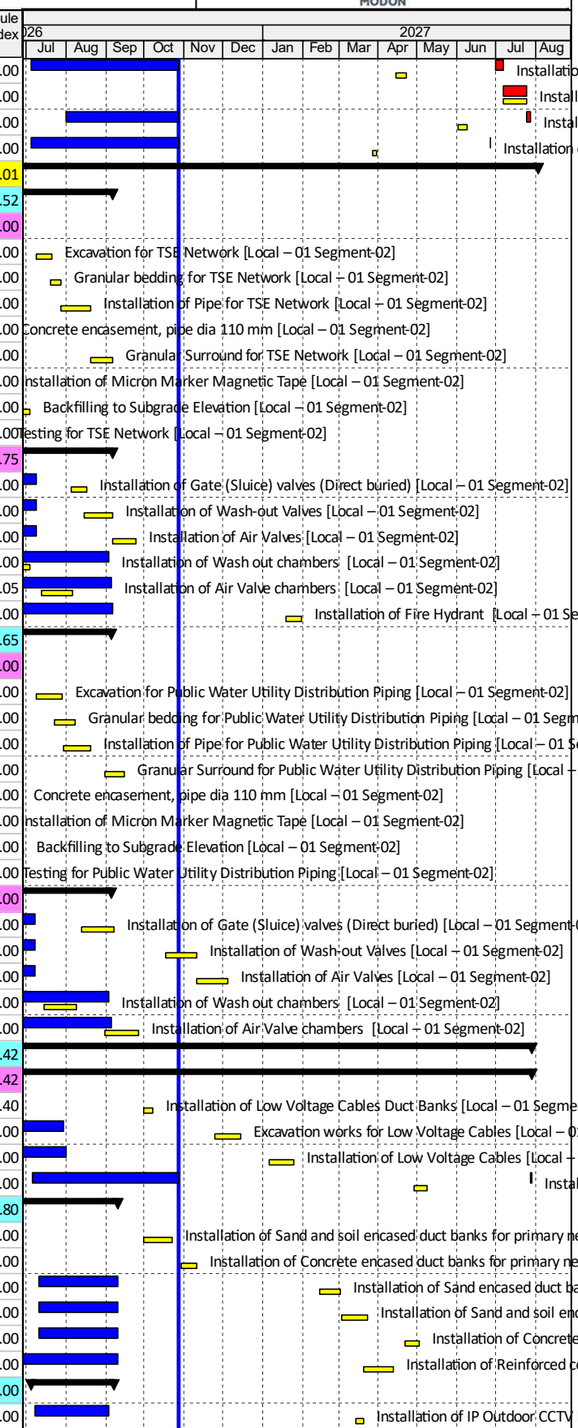


© Oracle Corporation

Activity ID	Activity Name	Original Duration	Budgeted Total Cost	BL Project Start	BL Project Finish	Actual Start	Actual Finish	Planned Value Cost	Earned Value Cost	Schedule Performance Index
CON-LEG101-LR-9700	Installation of Outdoor PTZ IP66 [Local – 01 Segment-02]	2	23,450.00	28-Jan-27	30-Jan-27	04-Jul-26	03-Sep-26	0.00	23,450.00	0.00
CON-LEG101-LR-9950	Installation of Short Range wireless point to point wireless bridge [Loca	7	17,420.00	31-Jan-27	07-Feb-27	04-Jul-26	03-Sep-26	0.00	17,420.00	0.00
CON-LEG101-LR-8560	Excavation works for Low Voltage Cables for CCTV feeding system and (	8	4,020.00	04-Jan-27	12-Jan-27	04-Jul-26	06-Sep-26	0.00	4,020.00	0.00
CON-LEG101-LR-8630	Installation of Low Voltage Cables for CCTV feeding system and GSM [L	8	18,626.25	13-Jan-27	21-Jan-27	04-Jul-26	07-Sep-26	0.00	18,626.25	0.00
Earthing System		6	0.00	08-Feb-27	18-Feb-27	07-Jul-26		0.00	0.00	0.00
CON-LEG101-LR-8290	Installation of Earthing for Distribution panels,SL feeder pillars, KWH, U	6	0.00	08-Feb-27	18-Feb-27	07-Jul-26		0.00	0.00	0.00
Road Lighting		114	200,196.00	16-Nov-26	22-Dec-26	28-Mar-26		0.00	200,196.00	0.00
CON-LEG101-LR-8190	Installation of Street Lighting Luminaire [Local – 01 Segment-02]	6	34,840.00	09-Dec-26	15-Dec-26	20-May-26	15-Aug-26	0.00	34,840.00	0.00
CON-LEG101-LR-8090	Installation of Lighting poles [Local – 01 Segment-02]	17	118,456.00	16-Nov-26	05-Dec-26	28-Mar-26	17-Aug-26	0.00	118,456.00	0.00
CON-LEG101-LR-8440	Installation of Street Lighting feeder pillars / Lighting panels [Local – 0	3	46,900.00	06-Dec-26	08-Dec-26	05-Jul-26	10-Sep-26	0.00	46,900.00	0.00
CON-LEG101-LR-8340	Installation of Earthing for Streetlighting feeders for every end pole circ	6	0.00	16-Dec-26	22-Dec-26	05-Aug-26		0.00	0.00	0.00
LOCAL - 01 Segment-03 (From 2+133 to 3+200)		318	1,602,750.30	15-Jul-26	13-Mar-27	14-Jan-26		415,226.73	1,466,230.42	3.53
TSE Network		198	443,622.80	15-Jul-26	14-Jan-27	14-Jan-26		231,634.16	440,942.80	1.90
Pipe Work		51	247,312.80	15-Jul-26	07-Nov-26	14-Jan-26	16-Apr-26	231,634.16	247,312.80	1.07
CON-LEG101-LR-1320	Excavation for TSE Network [Local – 01 Segment-03]	19	48,774.90	15-Jul-26	05-Aug-26	14-Jan-26	24-Jan-26	48,774.90	48,774.90	1.00
CON-LEG101-LR-1430	Granular bedding for TSE Network [Local – 01 Segment-03]	8	12,199.60	06-Aug-26	15-Aug-26	17-Jan-26	30-Mar-26	12,199.60	12,199.60	1.00
CON-LEG101-LR-1550	Installation of Pipe for TSE Network [Local – 01 Segment-03]	20	109,765.10	16-Aug-26	07-Sep-26	19-Jan-26	31-Mar-26	109,765.10	109,765.10	1.00
CON-LEG101-LR-1770	Concrete encasement, pipe dia 110 mm [Local – 01 Segment-03]	3	1,596.00	26-Sep-26	28-Sep-26	01-Apr-26	02-Apr-26	1,596.00	1,596.00	1.00
CON-LEG101-LR-1870	Granular Surround for TSE Network [Local – 01 Segment-03]	14	13,999.60	29-Sep-26	14-Oct-26	29-Jan-26	04-Apr-26	13,999.60	13,999.60	1.00
CON-LEG101-LR-1980	Installation of Micron Marker Magnetic Tape [Local – 01 Segment-03]	6	12,199.60	15-Oct-26	21-Oct-26	25-Feb-26	05-Apr-26	12,199.60	12,199.60	1.00
CON-LEG101-LR-2100	Backfilling to Subgrade Elevation [Local – 01 Segment-03]	14	24,389.00	22-Oct-26	07-Nov-26	26-Feb-26	06-Apr-26	8,710.36	24,389.00	2.80
CON-LEG101-LR-1660	Testing for TSE Network [Local – 01 Segment-03]	14	24,389.00	08-Sep-26	24-Sep-26	14-Apr-26	16-Apr-26	24,389.00	24,389.00	1.00
Valves/Chamber		198	196,310.00	08-Nov-26	14-Jan-27	04-Mar-26		0.00	193,630.00	0.00
CON-LEG101-LR-15050	Installation of Air Valves [Local – 01 Segment-03]	10	6,030.00	07-Dec-26	17-Dec-26	01-Apr-26	09-Jul-26	0.00	6,030.00	0.00
CON-LEG101-LR-2210	Installation of Gate (Sluice) valves (Direct buried) [Local – 01 Segment-(	19	44,220.00	25-Nov-26	16-Dec-26	04-Mar-26	09-Jul-26	0.00	44,220.00	0.00
CON-LEG101-LR-2330	Installation of Wash-out Valves [Local – 01 Segment-03]	15	8,040.00	17-Dec-26	03-Jan-27	01-Apr-26	09-Jul-26	0.00	8,040.00	0.00
CON-LEG101-LR-2480	Installation of Fire Hydrant [Local – 01 Segment-03]	10	84,420.00	04-Jan-27	14-Jan-27	04-Mar-26	29-Sep-26	0.00	84,420.00	0.00
CON-LEG101-LR-15040	Installation of Air Valve chambers [Local – 01 Segment-03]	10	26,800.00	25-Nov-26	06-Dec-26	01-Apr-26		0.00	25,460.00	0.00
CON-LEG101-LR-2630	Installation of Wash out chambers [Local – 01 Segment-03]	15	26,800.00	08-Nov-26	24-Nov-26	27-Apr-26		0.00	25,460.00	0.00
Public Water Utility Distribution		116	348,051.70	06-Aug-26	20-Jan-27	14-Jan-26		183,592.57	344,031.70	1.87
Pipe Work		60	222,091.70	06-Aug-26	18-Nov-26	14-Jan-26	11-Apr-26	183,592.57	222,091.70	1.21
CON-LEG101-LR-10060	Excavation for Public Water Utility Distribution Piping [Local – 01 Segme	17	43,517.60	06-Aug-26	25-Aug-26	14-Jan-26	24-Jan-26	43,517.60	43,517.60	1.00
CON-LEG101-LR-10160	Granular bedding for Public Water Utility Distribution Piping [Local – 01	13	10,881.80	26-Aug-26	09-Sep-26	17-Jan-26	30-Mar-26	10,881.80	10,881.80	1.00
CON-LEG101-LR-10260	Installation of Pipe for Public Water Utility Distribution Piping [Local – 0	18	97,911.90	10-Sep-26	01-Oct-26	19-Jan-26	31-Mar-26	97,911.90	97,911.90	1.00
CON-LEG101-LR-10460	Concrete encasement, pipe dia 110 mm [Local – 01 Segment-03]	3	4,501.00	18-Oct-26	20-Oct-26	10-Feb-26	01-Apr-26	4,501.00	4,501.00	1.00
CON-LEG101-LR-10560	Granular Surround for Public Water Utility Distribution Piping [Local – 0	13	10,881.80	21-Oct-26	04-Nov-26	18-Feb-26	02-Apr-26	5,022.37	10,881.80	2.17
CON-LEG101-LR-10660	Installation of Micron Marker Magnetic Tape [Local – 01 Segment-03]	2	10,881.80	05-Nov-26	07-Nov-26	25-Feb-26	04-Apr-26	0.00	10,881.80	0.00
CON-LEG101-LR-10760	Backfilling to Subgrade Elevation [Local – 01 Segment-03]	10	21,757.90	08-Nov-26	18-Nov-26	26-Feb-26	05-Apr-26	0.00	21,757.90	0.00
CON-LEG101-LR-10360	Testing for Public Water Utility Distribution Piping [Local – 01 Segment-	13	21,757.90	03-Oct-26	17-Oct-26	10-Mar-26	11-Apr-26	21,757.90	21,757.90	1.00
Valves/Chamber		116	125,960.00	08-Nov-26	20-Jan-27	01-Apr-26		0.00	121,940.00	0.00
CON-LEG101-LR-1020	Installation of Gate (Sluice) valves (Direct buried) [Local – 01 Segment-(	8	23,450.00	24-Dec-26	02-Jan-27	18-Apr-26	09-Jul-26	0.00	23,450.00	0.00
CON-LEG101-LR-1130	Installation of Wash-out Valves [Local – 01 Segment-03]	8	16,080.00	03-Jan-27	11-Jan-27	01-Apr-26	09-Jul-26	0.00	16,080.00	0.00
CON-LEG101-LR-1170	Installation of Air Valves [Local – 01 Segment-03]	8	6,030.00	12-Jan-27	20-Jan-27	01-Apr-26	09-Jul-26	0.00	6,030.00	0.00
CON-LEG101-LR-1230	Installation of Wash out chambers [Local – 01 Segment-03]	20	53,600.00	08-Nov-26	30-Nov-26	27-Apr-26		0.00	50,920.00	0.00
CON-LEG101-LR-1270	Installation of Air Valve chambers [Local – 01 Segment-03]	20	26,800.00	01-Dec-26	23-Dec-26	01-Apr-26		0.00	25,460.00	0.00
Electrical Works		106	174,562.60	19-Nov-26	16-Feb-27	31-May-26	17-Sep-26	0.00	174,562.60	0.00
Low Voltage		106	174,562.60	19-Nov-26	16-Feb-27	31-May-26	17-Sep-26	0.00	174,562.60	0.00
CON-LEG101-LR-8000	Installation of Low Voltage Cables Duct Banks [Local – 01 Segment-03]	7	16,961.50	09-Dec-26	16-Dec-26	31-May-26	04-Jun-26	0.00	16,961.50	0.00
CON-LEG101-LR-7800	Excavation works for Low Voltage Cables [Local – 01 Segment-03]	17	0.00	19-Nov-26	08-Dec-26	12-Aug-26	15-Sep-26	0.00	0.00	0.00
CON-LEG101-LR-7900	Installation of Low Voltage Cables [Local – 01 Segment-03]	17	155,591.10	17-Dec-26	05-Jan-27	12-Aug-26	16-Sep-26	0.00	155,591.10	0.00
CON-LEG101-LR-8780	Installation of Earthing System [Local – 01 Segment-03]	8	2,010.00	03-Feb-27	16-Feb-27	12-Aug-26	17-Sep-26	0.00	2,010.00	0.00
Telecommunications		76	359,401.95	19-Nov-26	03-Mar-27	31-May-26		0.00	234,272.07	0.00
CON-LEG101-LR-9250	Installation of Concrete encased duct banks for for combined network (	9	1,888.00	27-Jan-27	06-Feb-27	31-May-26	04-Jun-26	0.00	1,888.00	0.00

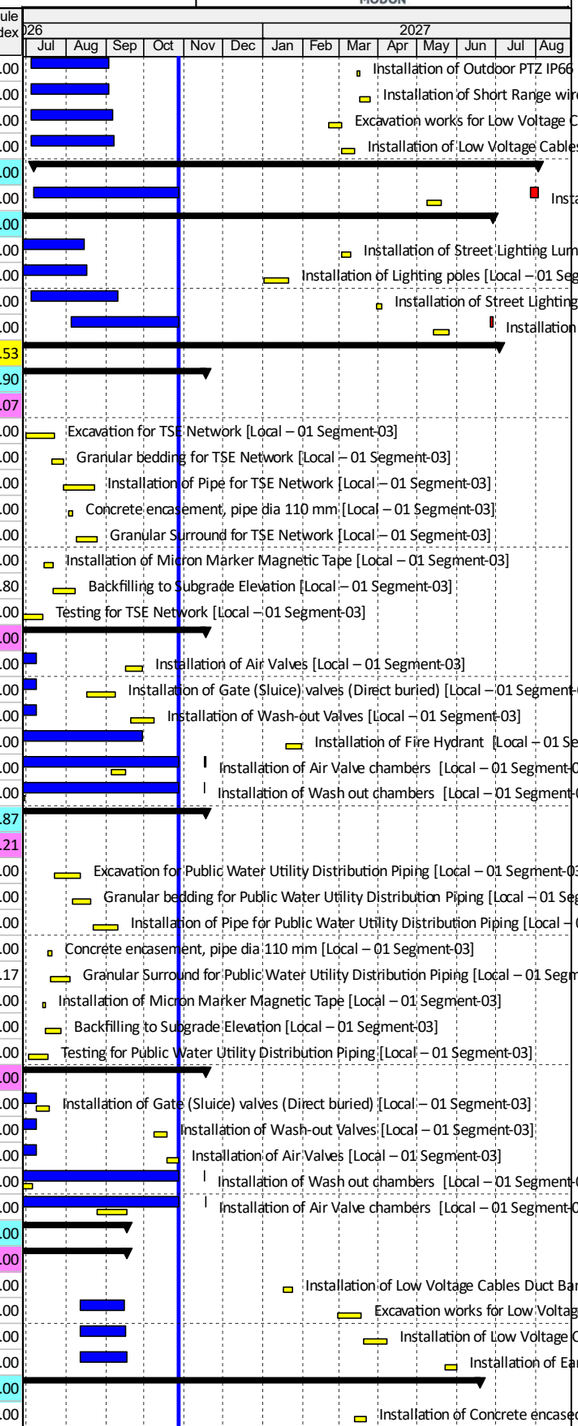


© Oracle Corporation

Activity ID	Activity Name	Original Duration	Budgeted Total Cost	BL Project Start	BL Project Finish	Actual Start	Actual Finish	Planned Value Cost	Earned Value Cost	Schedule Performance Index
CON-LEG101-LR-8850	Installation of Sand and soil encased duct banks for primary network [L	15	121,846.70	19-Nov-26	06-Dec-26	05-Sep-26		0.00	79,200.36	0.00
CON-LEG101-LR-8950	Installation of Concrete encased duct banks for primary network [Local	11	55,411.75	07-Dec-26	19-Dec-26	05-Sep-26		0.00	36,017.64	0.00
CON-LEG101-LR-9050	Installation of Sand encased duct banks for secondary network [Local –	14	25,969.00	20-Dec-26	04-Jan-27	05-Sep-26		0.00	16,879.85	0.00
CON-LEG101-LR-9150	Installation of Sand and soil encased duct banks, for combined network	18	6,216.50	06-Jan-27	26-Jan-27	05-Sep-26		0.00	4,040.73	0.00
CON-LEG101-LR-9350	Installation of Reinforced concrete manhole [Local – 01 Segment-03]	17	148,070.00	07-Feb-27	03-Mar-27	22-Aug-26		0.00	96,245.50	0.00
CCTV feeding system and GSM		31	76,915.25	05-Jan-27	23-Feb-27	06-Jul-26	01-Sep-26	0.00	76,915.25	0.00
CON-LEG101-LR-8570	Excavation works for Low Voltage Cables for CCTV feeding system and (	10	4,020.00	05-Jan-27	16-Jan-27	06-Jul-26	01-Sep-26	0.00	4,020.00	0.00
CON-LEG101-LR-8640	Installation of Low Voltage Cables for CCTV feeding system and GSM [L	10	18,625.25	21-Jan-27	01-Feb-27	06-Jul-26	01-Sep-26	0.00	18,625.25	0.00
CON-LEG101-LR-9630	Installation of IP Outdoor CCTV POE Camera,5 MP, Metal Housing [Loca	5	13,400.00	02-Feb-27	07-Feb-27	11-Jul-26	01-Sep-26	0.00	13,400.00	0.00
CON-LEG101-LR-9710	Installation of Outdoor PTZ IP66 [Local – 01 Segment-03]	2	23,450.00	08-Feb-27	14-Feb-27	06-Jul-26	01-Sep-26	0.00	23,450.00	0.00
CON-LEG101-LR-9960	Installation of Short Range wireless point to point wireless bridge [Loca	7	17,420.00	15-Feb-27	23-Feb-27	06-Jul-26	01-Sep-26	0.00	17,420.00	0.00
Earthing System		8	0.00	04-Mar-27	13-Mar-27			0.00	0.00	0.00
CON-LEG101-LR-8300	Installation of Earthing for Distribution panels,SL feeder pillars, KWH, U	8	0.00	04-Mar-27	13-Mar-27			0.00	0.00	0.00
Road Lighting		144	200,196.00	09-Dec-26	12-Jan-27	15-Mar-26		0.00	195,506.00	0.00
CON-LEG101-LR-8100	Installation of Lighting poles [Local – 01 Segment-03]	17	118,456.00	09-Dec-26	28-Dec-26	15-Mar-26	24-Oct-26	0.00	118,456.00	0.00
CON-LEG101-LR-8200	Installation of Street Lighting Luminaire [Local – 01 Segment-03]	6	34,840.00	29-Dec-26	04-Jan-27	12-Aug-26	24-Oct-26	0.00	34,840.00	0.00
CON-LEG101-LR-8350	Installation of Earthing for Streetlighting feeders for every end pole circ	6	0.00	06-Jan-27	12-Jan-27	05-Sep-26		0.00	0.00	0.00
CON-LEG101-LR-8450	Installation of Street Lighting feeder pillars / Lighting panels [Local – 0	7	46,900.00	29-Dec-26	05-Jan-27	12-Aug-26		0.00	42,210.00	0.00
Local – 02		343	1,617,805.55	16-Jun-26	06-Mar-27	04-Feb-26		735,641.58	1,389,034.05	1.89
TSE Network		230	388,563.40	16-Jun-26	14-Jan-27	04-Feb-26		328,263.40	385,481.40	1.17
Pipe Work		67	223,073.40	16-Jun-26	19-Sep-26	04-Feb-26	21-May-26	223,073.40	223,073.40	1.00
CON-LEG101-LR-1330	Excavation for TSE Network [Local – 02]	13	44,252.10	16-Jun-26	30-Jun-26	04-Feb-26	15-Feb-26	44,252.10	44,252.10	1.00
CON-LEG101-LR-1440	Granular bedding for TSE Network [Local – 02]	10	11,082.00	01-Jul-26	12-Jul-26	05-Feb-26	22-Apr-26	11,082.00	11,082.00	1.00
CON-LEG101-LR-1560	Installation of Pipe for TSE Network [Local – 02]	14	99,684.30	13-Jul-26	28-Jul-26	05-Feb-26	23-Apr-26	99,684.30	99,684.30	1.00
CON-LEG101-LR-1780	Concrete encasement, pipe dia 110 mm [Local – 02]	2	1,596.00	10-Aug-26	11-Aug-26	15-Mar-26	18-May-26	1,596.00	1,596.00	1.00
CON-LEG101-LR-1880	Granular Surround for TSE Network [Local – 02]	10	11,082.00	12-Aug-26	23-Aug-26	14-Feb-26	19-May-26	11,082.00	11,082.00	1.00
CON-LEG101-LR-2000	Installation of Micron Marker Magnetic Tape [Local – 02]	4	11,082.00	24-Aug-26	27-Aug-26	16-Mar-26	20-May-26	11,082.00	11,082.00	1.00
CON-LEG101-LR-1670	Testing for TSE Network [Local – 02]	10	22,147.50	29-Jul-26	09-Aug-26	18-Mar-26	21-May-26	22,147.50	22,147.50	1.00
CON-LEG101-LR-2110	Backfilling to Subgrade Elevation [Local – 02]	19	22,147.50	29-Aug-26	19-Sep-26	17-Mar-26	21-May-26	22,147.50	22,147.50	1.00
Valves/Chamber		210	165,490.00	29-Jul-26	14-Jan-27	29-Apr-26		105,190.00	162,408.00	1.54
CON-LEG101-LR-2220	Installation of Gate (Sluice) valves (Direct buried) [Local – 02]	13	43,550.00	23-Aug-26	06-Sep-26	29-Apr-26	05-Aug-26	43,550.00	43,550.00	1.00
CON-LEG101-LR-2490	Installation of Fire Hydrant [Local – 02]	10	60,300.00	04-Jan-27	14-Jan-27	20-May-26	04-Oct-26	0.00	60,300.00	0.00
CON-LEG101-LR-2410	Installation of Wash out Valves [Local – 02]	15	8,040.00	23-Aug-26	08-Sep-26	29-Apr-26		8,040.00	7,638.00	0.95
CON-LEG101-LR-2710	Installation of Wash out chambers [Local – 02]	21	53,600.00	29-Jul-26	22-Aug-26	29-Apr-26		53,600.00	50,920.00	0.95
Public Water Utility Distribution		63	249,770.30	01-Jul-26	06-Oct-26	04-Feb-26		249,770.30	245,917.80	0.98
Pipe Work		34	158,650.30	01-Jul-26	14-Sep-26	04-Feb-26	18-May-26	158,650.30	158,650.30	1.00
CON-LEG101-LR-10070	Excavation for Public Water Utility Distribution Piping [Local – 02]	12	30,828.60	01-Jul-26	14-Jul-26	04-Feb-26	15-Feb-26	30,828.60	30,828.60	1.00
CON-LEG101-LR-10170	Granular bedding for Public Water Utility Distribution Piping [Local – 02	9	7,707.60	15-Jul-26	25-Jul-26	05-Feb-26	22-Apr-26	7,707.60	7,707.60	1.00
CON-LEG101-LR-10270	Installation of Pipe for Public Water Utility Distribution Piping [Local – 0	13	69,367.50	26-Jul-26	09-Aug-26	05-Feb-26	23-Apr-26	69,367.50	69,367.50	1.00
CON-LEG101-LR-10370	Testing for Public Water Utility Distribution Piping [Local – 02]	9	15,415.20	10-Aug-26	19-Aug-26	13-May-26	14-May-26	15,415.20	15,415.20	1.00
CON-LEG101-LR-10470	Concrete encasement, pipe dia 110 mm [Local – 02]	2	4,501.00	20-Aug-26	22-Aug-26	15-Mar-26	16-May-26	4,501.00	4,501.00	1.00
CON-LEG101-LR-10570	Granular Surround for Public Water Utility Distribution Piping [Local – 0	9	7,707.60	23-Aug-26	01-Sep-26	14-Feb-26	16-May-26	7,707.60	7,707.60	1.00
CON-LEG101-LR-10670	Installation of Micron Marker Magnetic Tape [Local – 02]	3	7,707.60	02-Sep-26	05-Sep-26	16-Mar-26	17-May-26	7,707.60	7,707.60	1.00
CON-LEG101-LR-10770	Backfilling to Subgrade Elevation [Local – 02]	8	15,415.20	06-Sep-26	14-Sep-26	17-Mar-26	18-May-26	15,415.20	15,415.20	1.00
Valves/Chamber		56	91,120.00	10-Aug-26	06-Oct-26	01-Apr-26		91,120.00	87,267.50	0.96
CON-LEG101-LR-15090	Installation of Wash-out Valves [Local – 02]	8	8,040.00	09-Sep-26	17-Sep-26	29-Apr-26	05-Aug-26	8,040.00	8,040.00	1.00
CON-LEG101-LR-15100	Installation of Air Valves [Local – 02]	8	6,030.00	19-Sep-26	28-Sep-26	29-Apr-26	06-Aug-26	6,030.00	6,030.00	1.00
CON-LEG101-LR-1030	Installation of Gate (Sluice) valves (Direct buried) [Local – 02]	7	23,450.00	29-Sep-26	06-Oct-26	29-Apr-26		23,450.00	22,277.50	0.95
CON-LEG101-LR-15070	Installation of Wash out chambers [Local – 02]	20	26,800.00	10-Aug-26	01-Sep-26	29-Apr-26		26,800.00	25,460.00	0.95
CON-LEG101-LR-15080	Installation of Air Valve chambers [Local – 02]	20	26,800.00	02-Sep-26	26-Sep-26	01-Apr-26		26,800.00	25,460.00	0.95
Electrical Works		181	169,643.90	20-Sep-26	06-Mar-27	31-May-26		85,401.93	115,038.90	1.35
Low Voltage		181	169,643.90	20-Sep-26	06-Mar-27	31-May-26		85,401.93	115,038.90	1.35
CON-LEG101-LR-8010	Installation of Low Voltage Cables Duct Banks [Local – 02]	6	11,309.50	10-Oct-26	15-Oct-26	31-May-26	11-Jun-26	11,309.50	11,309.50	1.00

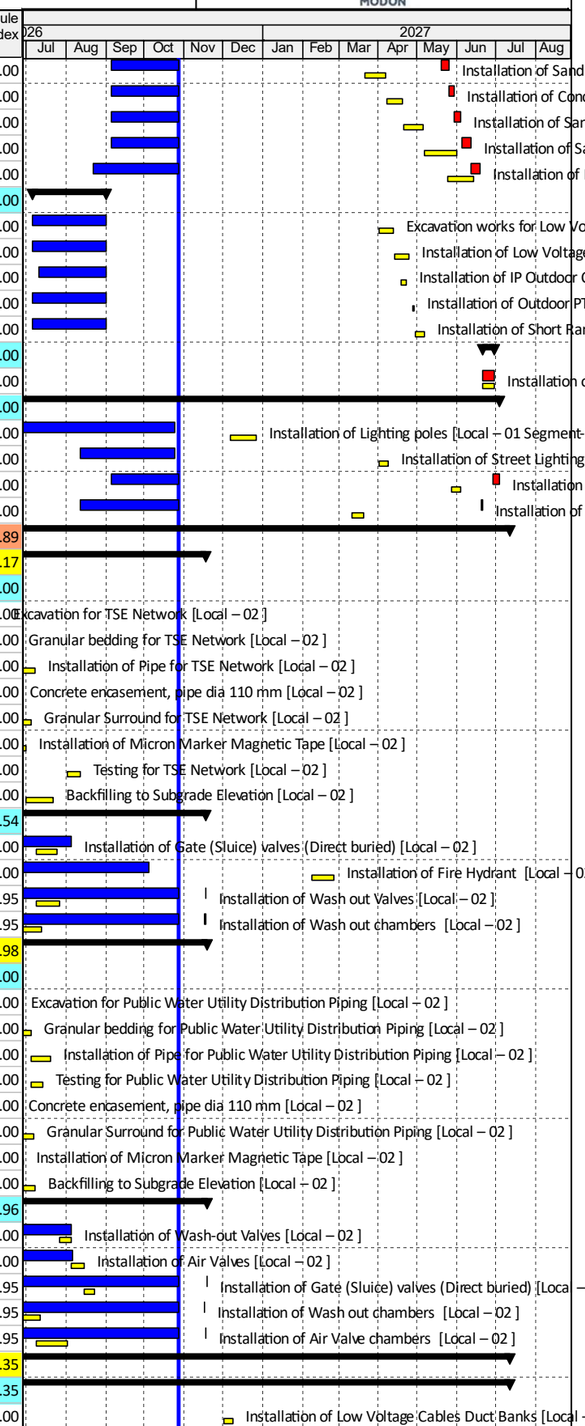


© Oracle Corporation

Activity ID	Activity Name	Original Duration	Budgeted Total Cost	BL Project Start	BL Project Finish	Actual Start	Actual Finish	Planned Value Cost	Earned Value Cost	Schedule Performance Index
CON-LEG101-LR-7810	Excavation works for Low Voltage Cables [Local – 02]	16	0.00	20-Sep-26	08-Oct-26	21-Jul-26	25-Jul-26	0.00	0.00	0.00
CON-LEG101-LR-7910	Installation of Low Voltage Cables [Local – 02]	14	103,729.40	17-Oct-26	01-Nov-26	24-Jul-26	01-Aug-26	74,092.43	103,729.40	1.40
CON-LEG101-LR-8490	Installation of Low Voltage Distribution Panel [Local – 02]	10	26,800.00	07-Nov-26	17-Nov-26			0.00	0.00	0.00
CON-LEG101-LR-8540	Installation of KWH Meters Walls [Local – 02]	7	26,800.00	24-Feb-27	03-Mar-27			0.00	0.00	0.00
CON-LEG101-LR-8790	Installation of Earthing System [Local – 02]	2	1,005.00	04-Mar-27	06-Mar-27			0.00	0.00	0.00
Telecommunications		102	254,799.95	10-Oct-26	10-Jan-27	31-May-26	08-Oct-26	72,205.96	254,799.95	3.53
CON-LEG101-LR-9260	Installation of Concrete encased duct banks for for combined network (	7	1,268.00	09-Dec-26	16-Dec-26	31-May-26	13-Jun-26	0.00	1,268.00	0.00
CON-LEG101-LR-8860	Installation of Sand and soil encased duct banks for primary network [L	18	81,231.70	10-Oct-26	29-Oct-26	31-May-26	01-Jul-26	72,205.96	81,231.70	1.13
CON-LEG101-LR-9360	Installation of Reinforced concrete manhole [Local – 02]	21	113,900.00	17-Dec-26	10-Jan-27	31-May-26	01-Jul-26	0.00	113,900.00	0.00
CON-LEG101-LR-8960	Installation of Concrete encased duct banks for primary network [Local	8	36,941.75	31-Oct-26	08-Nov-26	25-Aug-26	08-Oct-26	0.00	36,941.75	0.00
CON-LEG101-LR-9060	Installation of Sand encased duct banks for secondary network [Local –	10	17,314.00	09-Nov-26	19-Nov-26	25-Aug-26	08-Oct-26	0.00	17,314.00	0.00
CON-LEG101-LR-9160	Installation of Sand and soil encased duct banks, for combined network	16	4,144.50	21-Nov-26	08-Dec-26	25-Aug-26	08-Oct-26	0.00	4,144.50	0.00
CCTV feeding system and GSM		137	210,112.00	31-Oct-26	09-Jan-27	01-Jun-26		0.00	184,250.00	0.00
CON-LEG101-LR-9890	Installation of 25 Meters pole for CCTV Cameras [Local – 02]	7	87,100.00	24-Dec-26	31-Dec-26	01-Jun-26	16-Jul-26	0.00	87,100.00	0.00
CON-LEG101-LR-8580	Excavation works for Low Voltage Cables for CCTV feeding system and (	10	8,040.00	31-Oct-26	10-Nov-26	11-Jul-26	13-Sep-26	0.00	8,040.00	0.00
CON-LEG101-LR-8650	Installation of Low Voltage Cables for CCTV feeding system and GSM [L	7	37,252.00	11-Nov-26	18-Nov-26	11-Jul-26	14-Sep-26	0.00	37,252.00	0.00
CON-LEG101-LR-9470	Installation of 8POE ports Industrial Switches for remote poles [Local –	7	0.00	19-Nov-26	26-Nov-26	11-Jul-26		0.00	0.00	0.00
CON-LEG101-LR-9570	Installation of Server [Local – 02]	7	0.00	28-Nov-26	05-Dec-26	11-Jul-26		0.00	0.00	0.00
CON-LEG101-LR-9640	Installation of IP Outdoor CCTV POE Camera,5 MP, Metal Housing [Loca	7	16,750.00	06-Dec-26	13-Dec-26	11-Jul-26		0.00	15,075.00	0.00
CON-LEG101-LR-9720	Installation of Outdoor PTZ IP66 [Local – 02]	2	23,450.00	14-Dec-26	15-Dec-26	11-Jul-26		0.00	21,105.00	0.00
CON-LEG101-LR-9800	Installation of LED Screen 43" (24/7 operation) with Ethernet decoders	7	20,100.00	16-Dec-26	23-Dec-26			0.00	0.00	0.00
CON-LEG101-LR-9970	Installation of Short Range wireless point to point wireless bridge [Loca	7	17,420.00	02-Jan-27	09-Jan-27	11-Jul-26		0.00	15,678.00	0.00
Earthing System		6	21,440.00	18-Jan-27	24-Jan-27			0.00	0.00	0.00
CON-LEG101-LR-8310	Installation of Earthing for Distribution panels,SL feeder pillars, KWH, U	6	21,440.00	18-Jan-27	24-Jan-27			0.00	0.00	0.00
Road Lighting		171	323,476.00	09-Dec-26	23-Jan-27	15-Mar-26		0.00	203,546.00	0.00
CON-LEG101-LR-8110	Installation of Lighting poles [Local – 02]	7	118,456.00	09-Dec-26	16-Dec-26	15-Mar-26	17-Aug-26	0.00	118,456.00	0.00
CON-LEG101-LR-8210	Installation of Street Lighting Luminaire [Local – 02]	7	34,840.00	17-Dec-26	24-Dec-26	05-Jul-26	17-Aug-26	0.00	34,840.00	0.00
CON-LEG101-LR-7430	Installation of Unit Substation Including concrete foundations and fencir	7	56,950.00	17-Dec-26	24-Dec-26			0.00	0.00	0.00
CON-LEG101-LR-7510	Installation of Ring Main Unit RMU [Local – 02]	13	50,250.00	26-Dec-26	09-Jan-27			0.00	0.00	0.00
CON-LEG101-LR-8360	Installation of Earthing for Streetlighting feeders for every end pole circ	5	16,080.00	18-Jan-27	23-Jan-27	08-Aug-26		0.00	8,040.00	0.00
CON-LEG101-LR-8460	Installation of Street Lighting feeder pillars / Lighting panels [Local – 0	7	46,900.00	10-Jan-27	17-Jan-27	08-Jul-26		0.00	42,210.00	0.00
Local – 03		380	1,107,937.45	20-Jun-26	07-Mar-27	05-Feb-26		247,592.16	760,706.34	3.07
TSE Network		237	240,485.10	20-Jun-26	20-Jan-27	05-Feb-26		155,203.67	236,465.10	1.52
Pipe Work		52	97,775.10	20-Jun-26	18-Aug-26	05-Feb-26	30-Jun-26	97,775.10	97,775.10	1.00
CON-LEG101-LR-1340	Excavation for TSE Network [Local – 03]	6	17,797.80	20-Jun-26	25-Jun-26	05-Feb-26	16-Feb-26	17,797.80	17,797.80	1.00
CON-LEG101-LR-1460	Granular bedding for TSE Network [Local – 03]	7	4,899.00	27-Jun-26	04-Jul-26	15-Feb-26	03-Mar-26	4,899.00	4,899.00	1.00
CON-LEG101-LR-1570	Installation of Pipe for TSE Network [Local – 03]	13	44,090.10	05-Jul-26	19-Jul-26	18-Feb-26	15-Apr-26	44,090.10	44,090.10	1.00
CON-LEG101-LR-1680	Testing for TSE Network [Local – 03]	7	9,797.10	20-Jul-26	27-Jul-26	29-Apr-26	29-Apr-26	9,797.10	9,797.10	1.00
CON-LEG101-LR-1890	Granular Surround for TSE Network [Local – 03]	7	4,899.00	01-Aug-26	08-Aug-26	25-Feb-26	30-Apr-26	4,899.00	4,899.00	1.00
CON-LEG101-LR-1790	Concrete encasement, pipe dia 110 mm [Local – 03]	3	1,596.00	28-Jul-26	30-Jul-26	30-Apr-26	30-Apr-26	1,596.00	1,596.00	1.00
CON-LEG101-LR-2010	Installation of Micron Marker Magnetic Tape [Local – 03]	3	4,899.00	09-Aug-26	11-Aug-26	02-May-26	02-May-26	4,899.00	4,899.00	1.00
CON-LEG101-LR-2120	Backfilling to Subgrade Elevation [Local – 03]	6	9,797.10	12-Aug-26	18-Aug-26	03-May-26	30-Jun-26	9,797.10	9,797.10	1.00
Valves/Chamber		170	142,710.00	19-Sep-26	20-Jan-27	15-Apr-26		57,428.57	138,690.00	2.42
CON-LEG101-LR-2230	Installation of Gate (Sluice) valves (Direct buried) [Local – 03]	15	12,060.00	08-Nov-26	24-Nov-26	15-Apr-26	05-Aug-26	0.00	12,060.00	0.00
CON-LEG101-LR-2340	Installation of Wash-out Valves [Local – 03]	15	8,040.00	25-Nov-26	12-Dec-26	15-Apr-26	05-Aug-26	0.00	8,040.00	0.00
CON-LEG101-LR-2420	Installation of Air Valves [Local – 03]	15	12,060.00	13-Dec-26	29-Dec-26	15-Apr-26	05-Aug-26	0.00	12,060.00	0.00
CON-LEG101-LR-2500	Installation of Fire Hydrant [Local – 03]	15	30,150.00	04-Jan-27	20-Jan-27	15-Apr-26	05-Oct-26	0.00	30,150.00	0.00
CON-LEG101-LR-2640	Installation of Wash out chambers [Local – 03]	21	26,800.00	19-Sep-26	13-Oct-26	29-Apr-26		26,800.00	25,460.00	0.95
CON-LEG101-LR-2720	Installation of Air Valve chambers [Local – 03]	21	53,600.00	14-Oct-26	07-Nov-26	15-Apr-26		30,628.57	50,920.00	1.66
Public Water Utility Distribution		90	159,607.00	09-Aug-26	19-Dec-26	05-Feb-26		88,252.00	158,267.00	1.79
Pipe Work		20	88,252.00	09-Aug-26	12-Oct-26	05-Feb-26	30-Jun-26	88,252.00	88,252.00	1.00
CON-LEG101-LR-10080	Excavation for Public Water Utility Distribution Piping [Local – 03]	10	16,748.30	09-Aug-26	19-Aug-26	05-Feb-26	16-Feb-26	16,748.30	16,748.30	1.00
CON-LEG101-LR-10180	Granular bedding for Public Water Utility Distribution Piping [Local – 03	7	4,199.50	20-Aug-26	27-Aug-26	15-Feb-26	03-Mar-26	4,199.50	4,199.50	1.00

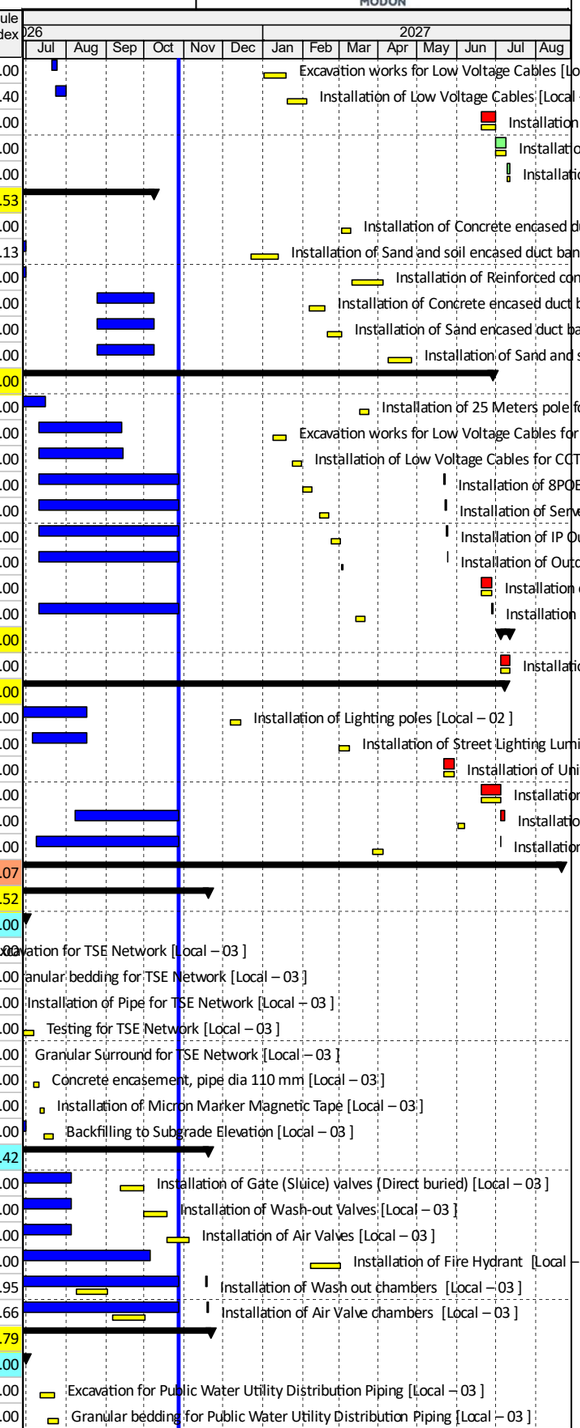


© Oracle Corporation

Activity ID	Activity Name	Original Duration	Budgeted Total Cost	BL Project Start	BL Project Finish	Actual Start	Actual Finish	Planned Value Cost	Earned Value Cost	Schedule Performance Index
CON-LEG101-LR-10280	Installation of Pipe for Public Water Utility Distribution Piping [Local – 0	12	37,685.60	29-Aug-26	10-Sep-26	18-Feb-26	14-Mar-26	37,685.60	37,685.60	1.00
CON-LEG101-LR-10380	Testing for Public Water Utility Distribution Piping [Local – 03]	7	8,373.70	12-Sep-26	19-Sep-26	29-Apr-26	29-Apr-26	8,373.70	8,373.70	1.00
CON-LEG101-LR-10580	Granular Surround for Public Water Utility Distribution Piping [Local – 0	7	4,188.70	24-Sep-26	01-Oct-26	25-Feb-26	30-Apr-26	4,188.70	4,188.70	1.00
CON-LEG101-LR-10480	Concrete encasement, pipe dia 110 mm [Local – 03]	3	4,501.00	20-Sep-26	22-Sep-26	30-Apr-26	30-Apr-26	4,501.00	4,501.00	1.00
CON-LEG101-LR-10680	Installation of Micron Marker Magnetic Tape [Local – 03]	3	4,188.70	03-Oct-26	05-Oct-26	02-May-26	25-Jun-26	4,188.70	4,188.70	1.00
CON-LEG101-LR-10780	Backfilling to Subgrade Elevation [Local – 03]	6	8,366.50	06-Oct-26	12-Oct-26	03-May-26	30-Jun-26	8,366.50	8,366.50	1.00
Valves/Chamber		23	71,355.00	08-Nov-26	19-Dec-26	15-Apr-26		0.00	70,015.00	0.00
CON-LEG101-LR-1040	Installation of Gate (Sluice) valves (Direct buried) [Local – 03]	8	38,525.00	10-Dec-26	19-Dec-26	15-Apr-26	05-Aug-26	0.00	38,525.00	0.00
CON-LEG101-LR-15120	Installation of Air Valves [Local – 03]	8	6,030.00	01-Dec-26	09-Dec-26	15-Apr-26	05-Aug-26	0.00	6,030.00	0.00
CON-LEG101-LR-15110	Installation of Air Valve chambers [Local – 03]	20	26,800.00	08-Nov-26	30-Nov-26	15-Apr-26		0.00	25,460.00	0.00
Electrical Works		164	81,532.80	13-Oct-26	24-Nov-26	18-Apr-26		791.65	7,916.50	10.00
Low Voltage		164	81,532.80	13-Oct-26	24-Nov-26	18-Apr-26		791.65	7,916.50	10.00
CON-LEG101-LR-8020	Installation of Low Voltage Cables Duct Banks [Local – 03]	10	7,916.50	27-Oct-26	07-Nov-26	18-Apr-26	07-May-26	791.65	7,916.50	10.00
CON-LEG101-LR-7820	Excavation works for Low Voltage Cables [Local – 03]	12	0.00	13-Oct-26	26-Oct-26			0.00	0.00	0.00
CON-LEG101-LR-7920	Installation of Low Voltage Cables [Local – 03]	12	72,611.30	08-Nov-26	21-Nov-26			0.00	0.00	0.00
CON-LEG101-LR-8800	Installation of Earthing System [Local – 03]	3	1,005.00	22-Nov-26	24-Nov-26			0.00	0.00	0.00
Telecommunications		178	144,180.55	27-Oct-26	28-Jan-27	15-Apr-26		3,344.84	93,246.94	27.88
CON-LEG101-LR-8970	Installation of Concrete encased duct banks for primary network [Local	6	25,858.25	25-Nov-26	01-Dec-26	22-Apr-26	10-May-26	0.00	25,858.25	0.00
CON-LEG101-LR-9370	Installation of Reinforced concrete manhole [Local – 03]	21	45,560.00	05-Jan-27	28-Jan-27	15-Apr-26	02-Jul-26	0.00	45,560.00	0.00
CON-LEG101-LR-8870	Installation of Sand and soil encased duct banks for primary network [L	17	56,862.30	27-Oct-26	15-Nov-26	21-Apr-26		3,344.84	17,058.69	5.10
CON-LEG101-LR-9070	Installation of Sand encased duct banks for secondary network [Local –	7	12,119.00	02-Dec-26	09-Dec-26	15-Oct-26		0.00	3,635.70	0.00
CON-LEG101-LR-9170	Installation of Sand and soil encased duct banks, for combined network	17	2,901.00	10-Dec-26	29-Dec-26	15-Oct-26		0.00	870.30	0.00
CON-LEG101-LR-9270	Installation of Concrete encased duct banks for for combined network (	5	880.00	30-Dec-26	04-Jan-27	15-Oct-26		0.00	264.00	0.00
CCTV feeding system and GSM		43	190,012.00	10-Dec-26	27-Feb-27	23-May-26		0.00	179,720.80	0.00
CON-LEG101-LR-9900	Installation of 25 Meters pole for CCTV Cameras [Local – 03]	10	87,100.00	30-Jan-27	14-Feb-27	23-May-26	08-Jul-26	0.00	87,100.00	0.00
CON-LEG101-LR-8590	Excavation works for Low Voltage Cables for CCTV feeding system and (	10	8,040.00	10-Dec-26	21-Dec-26	13-Jul-26		0.00	7,236.00	0.00
CON-LEG101-LR-8660	Installation of Low Voltage Cables for CCTV feeding system and GSM [L	12	37,252.00	22-Dec-26	04-Jan-27	13-Jul-26		0.00	33,526.80	0.00
CON-LEG101-LR-9480	Installation of 8POE ports Industrial Switches for remote poles [Local –	8	0.00	05-Jan-27	13-Jan-27	13-Jul-26		0.00	0.00	0.00
CON-LEG101-LR-9650	Installation of IP Outdoor CCTV POE Camera,5 MP, Metal Housing [Loca	5	16,750.00	14-Jan-27	19-Jan-27	13-Jul-26		0.00	15,075.00	0.00
CON-LEG101-LR-9730	Installation of Outdoor PTZ IP66 [Local – 03]	8	23,450.00	20-Jan-27	28-Jan-27	13-Jul-26		0.00	21,105.00	0.00
CON-LEG101-LR-9980	Installation of Short Range wireless point to point wireless bridge [Loca	10	17,420.00	15-Feb-27	27-Feb-27	23-May-26		0.00	15,678.00	0.00
Earthing System		7	21,440.00	28-Feb-27	07-Mar-27			0.00	0.00	0.00
CON-LEG101-LR-15170	Installation of Earthing for Distribution panels,SL feeder pillars, KWH, U	7	21,440.00	28-Feb-27	07-Mar-27			0.00	0.00	0.00
Road Lighting		196	270,680.00	17-Dec-26	21-Feb-27	18-Apr-26		0.00	85,090.00	0.00
CON-LEG101-LR-7440	Installation of Unit Substation Including concrete foundations and fencir	10	56,950.00	12-Jan-27	23-Jan-27	11-Jul-26		0.00	11,390.00	0.00
CON-LEG101-LR-7520	Installation of Ring Main Unit RMU [Local – 03]	15	50,250.00	24-Jan-27	14-Feb-27			0.00	0.00	0.00
CON-LEG101-LR-8120	Installation of Lighting poles [Local – 03]	15	113,900.00	17-Dec-26	03-Jan-27	18-Apr-26		0.00	56,950.00	0.00
CON-LEG101-LR-8220	Installation of Street Lighting Luminaire [Local – 03]	7	33,500.00	04-Jan-27	11-Jan-27	14-Oct-26		0.00	16,750.00	0.00
CON-LEG101-LR-8370	Installation of Earthing for Streetlighting feeders for every end pole circ	6	16,080.00	15-Feb-27	21-Feb-27			0.00	0.00	0.00
Local – 04		361	879,480.25	20-Aug-26	18-Mar-27	01-Feb-26		249,810.79	109,212.23	0.44
TSE Network		230	265,502.30	20-Aug-26	25-Feb-27	01-Feb-26		146,296.19	67,627.39	0.46
Pipe Work		138	122,792.30	20-Aug-26	29-Oct-26	01-Feb-26		120,772.38	67,627.39	0.56
CON-LEG101-LR-1350	Excavation for TSE Network [Local – 04]	12	24,239.00	20-Aug-26	02-Sep-26	01-Feb-26		24,239.00	21,815.10	0.90
CON-LEG101-LR-1470	Granular bedding for TSE Network [Local – 04]	6	6,059.40	03-Sep-26	09-Sep-26	15-Feb-26		6,059.40	4,847.52	0.80
CON-LEG101-LR-1580	Installation of Pipe for TSE Network [Local – 04]	12	54,540.10	10-Sep-26	24-Sep-26	17-Feb-26		54,540.10	28,360.85	0.52
CON-LEG101-LR-1690	Testing for TSE Network [Local – 04]	6	12,119.50	26-Sep-26	01-Oct-26			12,119.50	0.00	0.00
CON-LEG101-LR-1810	Concrete encasement, pipe dia 110 mm [Local – 04]	3	1,596.00	03-Oct-26	05-Oct-26			1,596.00	0.00	0.00
CON-LEG101-LR-1910	Granular Surround for TSE Network [Local – 04]	6	6,059.40	06-Oct-26	12-Oct-26	18-Feb-26		6,059.40	3,150.89	0.52
CON-LEG101-LR-2020	Installation of Micron Marker Magnetic Tape [Local – 04]	3	6,059.40	13-Oct-26	15-Oct-26	11-Mar-26		6,059.40	3,150.89	0.52
CON-LEG101-LR-2130	Backfilling to Subgrade Elevation [Local – 04]	12	12,119.50	17-Oct-26	29-Oct-26	14-Mar-26		10,099.58	6,302.14	0.62
Valves/Chamber		87	142,710.00	17-Oct-26	25-Feb-27			25,523.81	0.00	0.00
CON-LEG101-LR-15060	Installation of Wash-out Valve chambers [Local – 04]	21	26,800.00	10-Nov-26	03-Dec-26			0.00	0.00	0.00
CON-LEG101-LR-2240	Installation of Gate (Sluice) valves (Direct buried) [Local – 04]	9	18,090.00	20-Dec-26	29-Dec-26			0.00	0.00	0.00

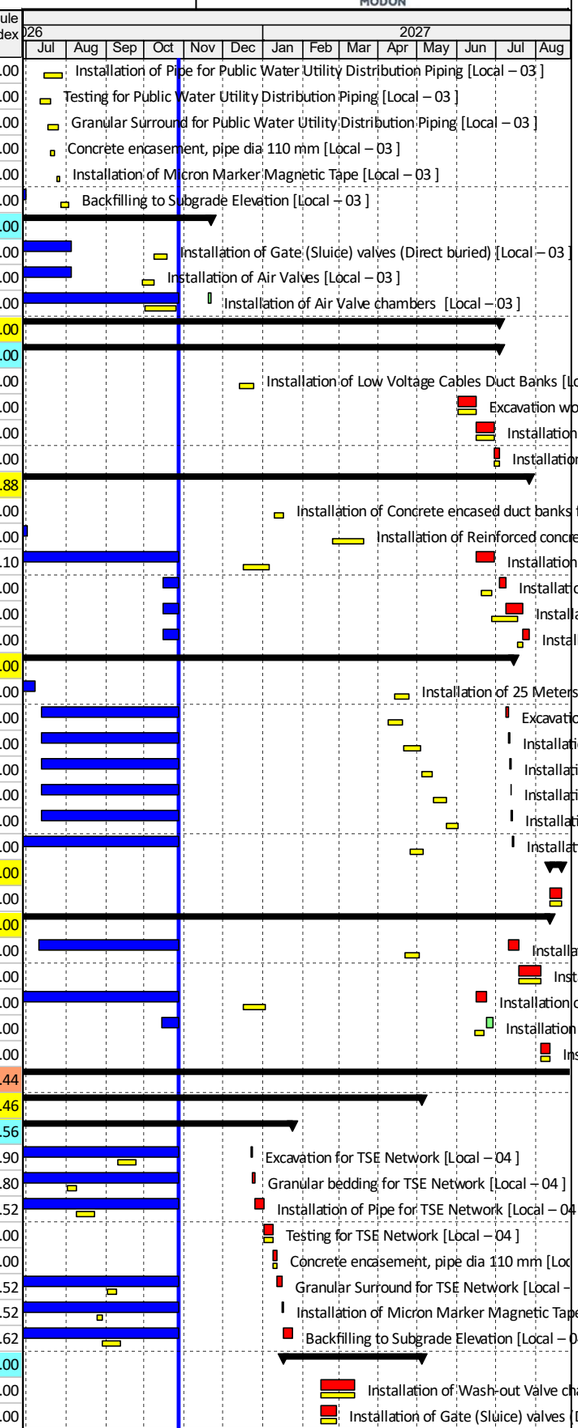


© Oracle Corporation

Activity ID	Activity Name	Original Duration	Budgeted Total Cost	BL Project Start	BL Project Finish	Actual Start	Actual Finish	Planned Value Cost	Earned Value Cost	Schedule Performance Index
CON-LEG101-LR-2350	Installation of Wash-out Valves [Local – 04]	15	8,040.00	30-Dec-26	16-Jan-27			0.00	0.00	0.00
CON-LEG101-LR-2430	Installation of Air Valves [Local – 04]	15	6,030.00	17-Jan-27	02-Feb-27			0.00	0.00	0.00
CON-LEG101-LR-2510	Installation of Fire Hydrant [Local – 04]	15	30,150.00	03-Feb-27	25-Feb-27			0.00	0.00	0.00
CON-LEG101-LR-2730	Installation of Air Valve chambers [Local – 04]	21	53,600.00	17-Oct-26	09-Nov-26			25,523.81	0.00	0.00
Public Water Utility Distribution		210	159,794.60	03-Sep-26	10-Jan-27	01-Feb-26		103,514.60	41,584.84	0.40
Pipe Work		142	103,514.60	03-Sep-26	26-Oct-26	01-Feb-26		103,514.60	41,584.84	0.40
CON-LEG101-LR-10090	Excavation for Public Water Utility Distribution Piping [Local – 04]	10	19,804.40	03-Sep-26	14-Sep-26	01-Feb-26		19,804.40	17,823.96	0.90
CON-LEG101-LR-10190	Granular bedding for Public Water Utility Distribution Piping [Local – 04	5	4,947.90	15-Sep-26	20-Sep-26	15-Feb-26		4,947.90	3,958.32	0.80
CON-LEG101-LR-10290	Installation of Pipe for Public Water Utility Distribution Piping [Local – 0	10	44,556.30	21-Sep-26	03-Oct-26	17-Feb-26		44,556.30	17,822.52	0.40
CON-LEG101-LR-10390	Testing for Public Water Utility Distribution Piping [Local – 04]	5	9,902.40	04-Oct-26	08-Oct-26			9,902.40	0.00	0.00
CON-LEG101-LR-10490	Concrete encasement, pipe dia 110 mm [Local – 04]	3	4,501.00	10-Oct-26	12-Oct-26			4,501.00	0.00	0.00
CON-LEG101-LR-10590	Granular Surround for Public Water Utility Distribution Piping [Local – 0	5	4,950.10	13-Oct-26	18-Oct-26	18-Feb-26		4,950.10	1,980.04	0.40
CON-LEG101-LR-10690	Installation of Micron Marker Magnetic Tape [Local – 04]	3	4,950.10	19-Oct-26	21-Oct-26			4,950.10	0.00	0.00
CON-LEG101-LR-10790	Backfilling to Subgrade Elevation [Local – 04]	4	9,902.40	22-Oct-26	26-Oct-26			9,902.40	0.00	0.00
Valves/Chamber		32	56,280.00	05-Dec-26	10-Jan-27			0.00	0.00	0.00
CON-LEG101-LR-1050	Installation of Gate (Sluice) valves (Direct buried) [Local – 04]	6	23,450.00	28-Dec-26	03-Jan-27			0.00	0.00	0.00
CON-LEG101-LR-1180	Installation of Air Valves [Local – 04]	6	6,030.00	04-Jan-27	10-Jan-27			0.00	0.00	0.00
CON-LEG101-LR-1280	Installation of Air Valve chambers [Local – 04]	20	26,800.00	05-Dec-26	27-Dec-26			0.00	0.00	0.00
Electrical Works		39	81,532.80	31-Oct-26	14-Dec-26			0.00	0.00	0.00
Low Voltage		39	81,532.80	31-Oct-26	14-Dec-26			0.00	0.00	0.00
CON-LEG101-LR-7830	Excavation works for Low Voltage Cables [Local – 04]	13	0.00	31-Oct-26	14-Nov-26			0.00	0.00	0.00
CON-LEG101-LR-7930	Installation of Low Voltage Cables [Local – 04]	13	72,611.30	26-Nov-26	10-Dec-26			0.00	0.00	0.00
CON-LEG101-LR-8030	Installation of Low Voltage Cables Duct Banks [Local – 04]	10	7,916.50	15-Nov-26	25-Nov-26			0.00	0.00	0.00
CON-LEG101-LR-8810	Installation of Earthing System [Local – 04]	3	1,005.00	12-Dec-26	14-Dec-26			0.00	0.00	0.00
Telecommunications		74	144,180.55	26-Nov-26	25-Feb-27			0.00	0.00	0.00
CON-LEG101-LR-8880	Installation of Sand and soil encased duct banks for primary network [L	17	56,862.30	26-Nov-26	15-Dec-26			0.00	0.00	0.00
CON-LEG101-LR-8980	Installation of Concrete encased duct banks for primary network [Local	6	25,858.25	16-Dec-26	22-Dec-26			0.00	0.00	0.00
CON-LEG101-LR-9080	Installation of Sand encased duct banks for secondary network [Local –	7	12,119.00	23-Dec-26	30-Dec-26			0.00	0.00	0.00
CON-LEG101-LR-9180	Installation of Sand and soil encased duct banks, for combined network	18	2,901.00	31-Dec-26	20-Jan-27			0.00	0.00	0.00
CON-LEG101-LR-9280	Installation of Concrete encased duct banks for for combined network	5	880.00	21-Jan-27	26-Jan-27			0.00	0.00	0.00
CON-LEG101-LR-9380	Installation of Reinforced concrete manhole [Local – 04]	21	45,560.00	27-Jan-27	25-Feb-27			0.00	0.00	0.00
CCTV feeding system and GSM		62	92,862.00	16-Dec-26	03-Mar-27			0.00	0.00	0.00
CON-LEG101-LR-8600	Excavation works for Low Voltage Cables for CCTV feeding system and	12	8,040.00	16-Dec-26	29-Dec-26			0.00	0.00	0.00
CON-LEG101-LR-8670	Installation of Low Voltage Cables for CCTV feeding system and GSM [L	13	37,252.00	30-Dec-26	13-Jan-27			0.00	0.00	0.00
CON-LEG101-LR-9490	Installation of 8POE ports Industrial Switches for remote poles [Local –	7	0.00	14-Jan-27	21-Jan-27			0.00	0.00	0.00
CON-LEG101-LR-9660	Installation of IP Outdoor CCTV POE Camera,5 MP, Metal Housing [Loca	8	6,700.00	23-Jan-27	31-Jan-27			0.00	0.00	0.00
CON-LEG101-LR-9740	Installation of Outdoor PTZ IP66 [Local – 04]	10	23,450.00	01-Feb-27	16-Feb-27			0.00	0.00	0.00
CON-LEG101-LR-9990	Installation of Short Range wireless point to point wireless bridge [Loca	12	17,420.00	17-Feb-27	03-Mar-27			0.00	0.00	0.00
Earthing System		8	0.00	10-Mar-27	18-Mar-27			0.00	0.00	0.00
CON-LEG101-LR-15160	Installation of Earthing for Distribution panels,SL feeder pillars, KWH, U	8	0.00	10-Mar-27	18-Mar-27			0.00	0.00	0.00
Road Lighting		61	135,608.00	04-Jan-27	09-Mar-27			0.00	0.00	0.00
CON-LEG101-LR-7450	Installation of Unit Substation Including concrete foundations and fencir	7	0.00	01-Feb-27	08-Feb-27			0.00	0.00	0.00
CON-LEG101-LR-7530	Installation of Ring Main Unit RMU [Local – 04]	14	0.00	14-Feb-27	02-Mar-27			0.00	0.00	0.00
CON-LEG101-LR-8130	Installation of Lighting poles [Local – 04]	18	104,788.00	04-Jan-27	24-Jan-27			0.00	0.00	0.00
CON-LEG101-LR-8230	Installation of Street Lighting Luminaire [Local – 04]	6	30,820.00	25-Jan-27	31-Jan-27			0.00	0.00	0.00
CON-LEG101-LR-8380	Installation of Earthing for Streetlighting feeders for every end pole circ	6	0.00	03-Mar-27	09-Mar-27			0.00	0.00	0.00
Local – 05		330	1,374,698.25	30-Aug-26	18-Mar-27	15-Mar-26		173,342.23	1,299,635.23	7.50
TSE Network		201	388,239.50	30-Aug-26	18-Mar-27	24-Mar-26		173,342.23	385,023.50	2.22
Pipe Work		49	168,144.50	30-Aug-26	29-Nov-26	24-Mar-26	23-Jun-26	137,608.90	168,144.50	1.22
CON-LEG101-LR-1370	Excavation for TSE Network [Local – 05]	12	33,306.50	30-Aug-26	12-Sep-26	24-Mar-26	16-Apr-26	33,306.50	33,306.50	1.00
CON-LEG101-LR-1480	Granular bedding for TSE Network [Local – 05]	9	8,327.70	13-Sep-26	22-Sep-26	30-Mar-26	18-Apr-26	8,327.70	8,327.70	1.00
CON-LEG101-LR-1590	Installation of Pipe for TSE Network [Local – 05]	15	74,946.70	24-Sep-26	11-Oct-26	01-Apr-26	20-Apr-26	74,946.70	74,946.70	1.00
CON-LEG101-LR-1700	Testing for TSE Network [Local – 05]	9	16,656.10	12-Oct-26	21-Oct-26	27-Apr-26	28-Apr-26	16,656.10	16,656.10	1.00

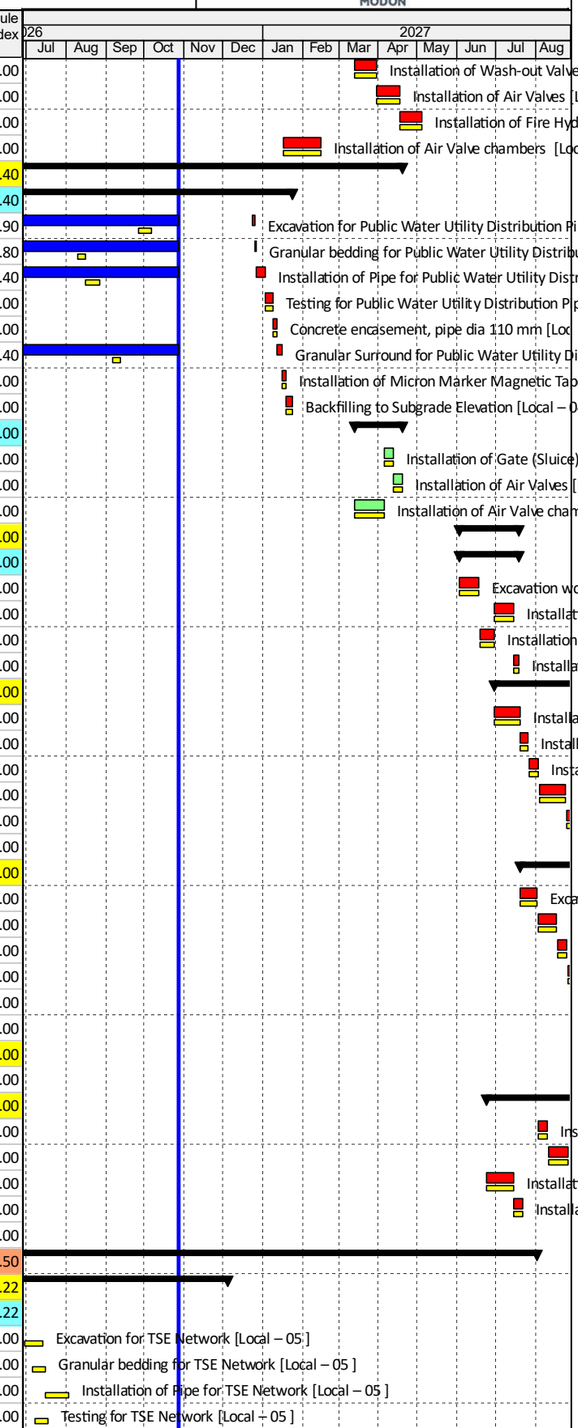

© Oracle Corporation

Activity ID	Activity Name	Original Duration	Budgeted Total Cost	BL Project Start	BL Project Finish	Actual Start	Actual Finish	Planned Value Cost	Earned Value Cost	Schedule Performance Index
CON-LEG101-LR-1820	Concrete encasement, pipe dia 110 mm [Local – 05]	2	1,596.00	22-Oct-26	24-Oct-26	29-Apr-26	20-Jun-26	1,596.00	1,596.00	1.00
CON-LEG101-LR-1920	Granular Surround for TSE Network [Local – 05]	9	8,327.70	25-Oct-26	03-Nov-26	30-Apr-26	21-Jun-26	2,775.90	8,327.70	3.00
CON-LEG101-LR-2030	Installation of Micron Marker Magnetic Tape [Local – 05]	4	8,327.70	04-Nov-26	08-Nov-26	02-May-26	22-Jun-26	0.00	8,327.70	0.00
CON-LEG101-LR-2140	Backfilling to Subgrade Elevation [Local – 05]	18	16,656.10	09-Nov-26	29-Nov-26	03-May-26	23-Jun-26	0.00	16,656.10	0.00
Valves/Chamber		195	220,095.00	12-Oct-26	18-Mar-27	04-Apr-26		35,733.33	216,879.00	6.07
CON-LEG101-LR-2250	Installation of Gate (Sluice) valves (Direct buried) [Local – 05]	14	30,485.00	11-Jan-27	26-Jan-27	25-Apr-26	08-Aug-26	0.00	30,485.00	0.00
CON-LEG101-LR-2360	Installation of Wash-out Valves [Local – 05]	14	16,080.00	27-Jan-27	16-Feb-27	25-Apr-26	08-Aug-26	0.00	16,080.00	0.00
CON-LEG101-LR-2440	Installation of Air Valves [Local – 05]	14	12,060.00	17-Feb-27	06-Mar-27	25-Apr-26	08-Aug-26	0.00	12,060.00	0.00
CON-LEG101-LR-2520	Installation of Fire Hydrant [Local – 05]	11	54,270.00	07-Mar-27	18-Mar-27	25-Apr-26	30-Sep-26	0.00	54,270.00	0.00
CON-LEG101-LR-2660	Installation of Wash out chambers [Local – 05]	21	53,600.00	12-Oct-26	04-Nov-26	30-Apr-26		35,733.33	51,992.00	1.46
CON-LEG101-LR-2740	Installation of Air Valve chambers [Local – 05]	21	53,600.00	05-Nov-26	29-Nov-26	04-Apr-26		0.00	51,992.00	0.00
Public Water Utility Distribution		54	181,681.20	30-Nov-26	04-Mar-27	24-Mar-26		0.00	181,681.20	0.00
Pipe Work		53	149,186.20	30-Nov-26	04-Mar-27	24-Mar-26	03-May-26	0.00	149,186.20	0.00
CON-LEG101-LR-10100	Excavation for Public Water Utility Distribution Piping [Local – 05]	13	28,937.20	30-Nov-26	14-Dec-26	24-Mar-26	21-Apr-26	0.00	28,937.20	0.00
CON-LEG101-LR-10200	Granular bedding for Public Water Utility Distribution Piping [Local – 05	10	7,233.30	15-Dec-26	26-Dec-26	30-Mar-26	22-Apr-26	0.00	7,233.30	0.00
CON-LEG101-LR-10300	Installation of Pipe for Public Water Utility Distribution Piping [Local – 0	14	65,108.90	27-Dec-26	11-Jan-27	01-Apr-26	23-Apr-26	0.00	65,108.90	0.00
CON-LEG101-LR-10400	Testing for Public Water Utility Distribution Piping [Local – 05]	10	14,469.60	12-Jan-27	23-Jan-27	27-Apr-26	28-Apr-26	0.00	14,469.60	0.00
CON-LEG101-LR-10500	Concrete encasement, pipe dia 110 mm [Local – 05]	7	4,501.00	24-Jan-27	31-Jan-27	29-Apr-26	29-Apr-26	0.00	4,501.00	0.00
CON-LEG101-LR-10600	Granular Surround for Public Water Utility Distribution Piping [Local – 0	10	7,233.30	01-Feb-27	16-Feb-27	30-Apr-26	30-Apr-26	0.00	7,233.30	0.00
CON-LEG101-LR-10700	Installation of Micron Marker Magnetic Tape [Local – 05]	3	7,233.30	17-Feb-27	20-Feb-27	02-May-26	02-May-26	0.00	7,233.30	0.00
CON-LEG101-LR-10800	Backfilling to Subgrade Elevation [Local – 05]	10	14,469.60	21-Feb-27	04-Mar-27	03-May-26	03-May-26	0.00	14,469.60	0.00
Valves/Chamber		37	32,495.00	12-Jan-27	04-Mar-27	25-Apr-26		0.00	32,495.00	0.00
CON-LEG101-LR-1060	Installation of Gate (Sluice) valves (Direct buried) [Local – 05]	10	32,495.00	04-Feb-27	20-Feb-27	25-Apr-26	08-Aug-26	0.00	32,495.00	0.00
CON-LEG101-LR-1140	Installation of Wash-out Valves [Local – 05]	10	0.00	21-Feb-27	04-Mar-27	25-Apr-26	08-Aug-26	0.00	0.00	0.00
CON-LEG101-LR-1240	Installation of Wash out chambers [Local – 05]	20	0.00	12-Jan-27	03-Feb-27	30-Apr-26		0.00	0.00	0.00
Electrical Works		121	138,043.50	30-Nov-26	18-Jan-27	02-May-26		0.00	138,043.50	0.00
Low Voltage		121	138,043.50	30-Nov-26	18-Jan-27	02-May-26		0.00	138,043.50	0.00
CON-LEG101-LR-8040	Installation of Low Voltage Cables Duct Banks [Local – 05]	6	13,567.50	24-Dec-26	30-Dec-26	02-May-26	07-May-26	0.00	13,567.50	0.00
CON-LEG101-LR-7840	Excavation works for Low Voltage Cables [Local – 05]	21	0.00	30-Nov-26	23-Dec-26	30-Jul-26	17-Aug-26	0.00	0.00	0.00
CON-LEG101-LR-7940	Installation of Low Voltage Cables [Local – 05]	14	124,476.00	31-Dec-26	16-Jan-27	02-Aug-26	17-Aug-26	0.00	124,476.00	0.00
CON-LEG101-LR-8820	Installation of Earthing System [Local – 05]	2	0.00	17-Jan-27	18-Jan-27			0.00	0.00	0.00
Telecommunications		104	271,567.80	30-Nov-26	30-Jan-27	02-May-26		0.00	245,870.40	0.00
CON-LEG101-LR-8990	Installation of Concrete encased duct banks for primary network [Local	8	44,324.50	12-Dec-26	20-Dec-26	02-May-26	07-May-26	0.00	44,324.50	0.00
CON-LEG101-LR-9290	Installation of Concrete encased duct banks for for combined network (	7	1,512.00	11-Jan-27	18-Jan-27	02-May-26	20-May-26	0.00	1,512.00	0.00
CON-LEG101-LR-8890	Installation of Sand and soil encased duct banks for primary network [L	10	97,477.30	30-Nov-26	10-Dec-26	02-May-26	04-Jul-26	0.00	97,477.30	0.00
CON-LEG101-LR-9090	Installation of Sand encased duct banks for secondary network [Local –	8	20,775.00	21-Dec-26	29-Dec-26	05-Sep-26		0.00	8,310.00	0.00
CON-LEG101-LR-9190	Installation of Sand and soil encased duct banks, for combined network	10	4,969.00	30-Dec-26	10-Jan-27	05-Sep-26		0.00	1,987.60	0.00
CON-LEG101-LR-9390	Installation of Reinforced concrete manhole [Local – 05]	10	102,510.00	19-Jan-27	30-Jan-27	02-May-26		0.00	92,259.00	0.00
CCTV feeding system and GSM		95	277,246.25	12-Dec-26	10-Mar-27	25-May-26		0.00	231,096.63	0.00
CON-LEG101-LR-9910	Installation of 25 Meters pole for CCTV Cameras [Local – 05]	4	87,100.00	04-Mar-27	08-Mar-27	25-May-26	08-Jul-26	0.00	87,100.00	0.00
CON-LEG101-LR-8610	Excavation works for Low Voltage Cables for CCTV feeding system and (	4	4,020.00	12-Dec-26	15-Dec-26	15-Jul-26		0.00	3,618.00	0.00
CON-LEG101-LR-8680	Installation of Low Voltage Cables for CCTV feeding system and GSM [L	6	18,626.25	16-Dec-26	22-Dec-26	15-Jul-26		0.00	16,763.63	0.00
CON-LEG101-LR-9440	Installation of Fiber Optic Patch Panel 12 port [Local – 05]	4	6,700.00	23-Dec-26	27-Dec-26	15-Jul-26		0.00	6,030.00	0.00
CON-LEG101-LR-9500	Installation of 8POE ports Industrial Switches for remote poles [Local –	3	20,100.00	28-Dec-26	30-Dec-26	15-Jul-26		0.00	18,090.00	0.00
CON-LEG101-LR-9530	Installation of Core Switch [Local – 05]	8	20,100.00	17-Jan-27	25-Jan-27	15-Jul-26		0.00	18,090.00	0.00
CON-LEG101-LR-9550	Installation of Access Switch 48 port [Local – 05]	4	10,050.00	26-Jan-27	30-Jan-27	15-Jul-26		0.00	9,045.00	0.00
CON-LEG101-LR-9580	Installation of Server [Local – 05]	3	43,550.00	31-Jan-27	02-Feb-27	15-Jul-26		0.00	39,195.00	0.00
CON-LEG101-LR-9600	Installation of Stand rack 42U- 19" [Local – 05]	3	10,050.00	03-Feb-27	06-Feb-27			0.00	0.00	0.00
CON-LEG101-LR-9670	Installation of IP Outdoor CCTV POE Camera,5 MP, Metal Housing [Loca	4	6,700.00	07-Feb-27	15-Feb-27	15-Jul-26		0.00	6,030.00	0.00
CON-LEG101-LR-9750	Installation of Outdoor PTZ IP66 [Local – 05]	3	23,450.00	16-Feb-27	18-Feb-27	15-Jul-26		0.00	21,105.00	0.00
CON-LEG101-LR-9810	Installation of LED Screen 43" (24/7 operation) with Ethernet decoders	2	20,100.00	20-Feb-27	21-Feb-27			0.00	0.00	0.00
CON-LEG101-LR-9860	Installation of Horizontal Power Distribution Unit (min 8 outlets) [Local	3	6,700.00	01-Mar-27	03-Mar-27	15-Jul-26		0.00	6,030.00	0.00
CON-LEG101-LR-10000	Installation of Short Range wireless point to point wireless bridge [Loca	2	0.00	09-Mar-27	10-Mar-27	15-Jul-26		0.00	0.00	0.00

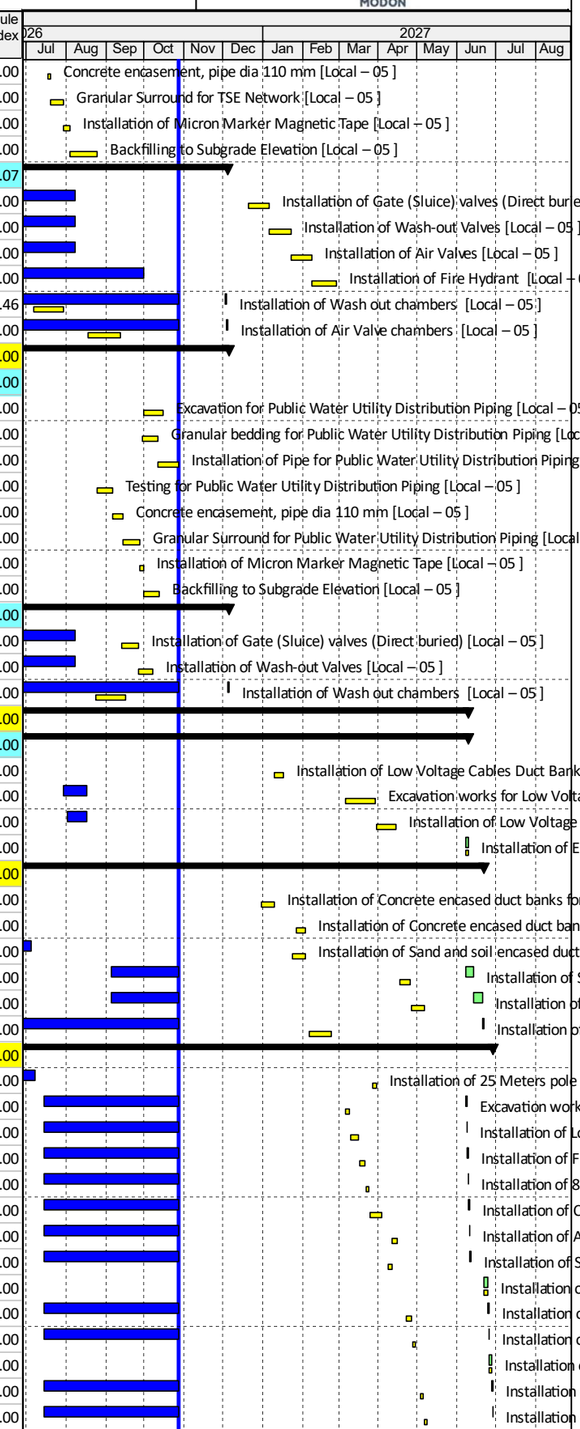

© Oracle Corporation

ENJAZCO

Tel: 4108184 - 4108180
Email: info@enjaz-co.com


JDH1-02-003 - Infrastructure Development For Industrial City 1 In Jeddah - Update - 27.10.2026

Progress Tracker

egis


MODON

Activity ID	Activity Name	Original Duration	Budgeted Total Cost	BL Project Start	BL Project Finish	Actual Start	Actual Finish	Planned Value Cost	Earned Value Cost	Schedule Performance Index
Earthing System		2	0.00	11-Mar-27	13-Mar-27			0.00	0.00	0.00
CON-LEG101-LR-15150	Installation of Earthing for Distribution panels,SL feeder pillars, KWH, U	2	0.00	11-Mar-27	13-Mar-27			0.00	0.00	0.00
Road Lighting		152	117,920.00	25-Jan-27	16-Mar-27	15-Mar-26		0.00	117,920.00	0.00
CON-LEG101-LR-8140	Installation of Lighting poles [Local – 05]	20	91,120.00	25-Jan-27	21-Feb-27	15-Mar-26	17-Aug-26	0.00	91,120.00	0.00
CON-LEG101-LR-8240	Installation of Street Lighting Luminaire [Local – 05]	5	26,800.00	23-Feb-27	28-Feb-27	01-Aug-26	17-Aug-26	0.00	26,800.00	0.00
CON-LEG101-LR-7460	Installation of Unit Substation Including concrete foundations and fencir	7	0.00	23-Feb-27	02-Mar-27	15-Jul-26		0.00	0.00	0.00
CON-LEG101-LR-7540	Installation of Ring Main Unit RMU [Local – 05]	7	0.00	03-Mar-27	10-Mar-27			0.00	0.00	0.00
CON-LEG101-LR-8390	Installation of Earthing for Streetlighting feeders for every end pole circ	5	0.00	11-Mar-27	16-Mar-27	10-Aug-26		0.00	0.00	0.00
Local – 06		317	820,882.00	31-Aug-26	18-Mar-27	16-Mar-26		120,213.56	814,433.70	6.77
TSE Network		65	201,349.00	31-Aug-26	07-Dec-26	01-Apr-26	03-Sep-26	120,213.56	201,349.00	1.67
Pipe Work		65	130,329.00	31-Aug-26	09-Nov-26	01-Apr-26	23-Jun-26	120,213.56	130,329.00	1.08
CON-LEG101-LR-1380	Excavation for TSE Network [Local – 06]	10	25,741.80	31-Aug-26	10-Sep-26	01-Apr-26	12-Apr-26	25,741.80	25,741.80	1.00
CON-LEG101-LR-1490	Granular bedding for TSE Network [Local – 06]	7	6,437.70	12-Sep-26	19-Sep-26	13-Apr-26	21-May-26	6,437.70	6,437.70	1.00
CON-LEG101-LR-1600	Installation of Pipe for TSE Network [Local – 06]	10	57,929.70	20-Sep-26	01-Oct-26	15-Apr-26	24-May-26	57,929.70	57,929.70	1.00
CON-LEG101-LR-1710	Testing for TSE Network [Local – 06]	7	12,874.20	03-Oct-26	10-Oct-26	13-Jun-26	14-Jun-26	12,874.20	12,874.20	1.00
CON-LEG101-LR-1830	Concrete encasement, pipe dia 110 mm [Local – 06]	2	1,596.00	11-Oct-26	12-Oct-26	15-Jun-26	17-Jun-26	1,596.00	1,596.00	1.00
CON-LEG101-LR-1930	Granular Surround for TSE Network [Local – 06]	7	6,437.70	13-Oct-26	20-Oct-26	16-Jun-26	17-Jun-26	6,437.70	6,437.70	1.00
CON-LEG101-LR-2040	Installation of Micron Marker Magnetic Tape [Local – 06]	3	6,437.70	21-Oct-26	24-Oct-26	18-Jun-26	18-Jun-26	6,437.70	6,437.70	1.00
CON-LEG101-LR-2150	Backfilling to Subgrade Elevation [Local – 06]	14	12,874.20	25-Oct-26	09-Nov-26	20-Jun-26	23-Jun-26	2,758.76	12,874.20	4.67
Valves/Chamber		22	71,020.00	10-Nov-26	07-Dec-26	13-May-26	03-Sep-26	0.00	71,020.00	0.00
CON-LEG101-LR-2260	Installation of Gate (Sluice) valves (Direct buried) [Local – 06]	9	28,810.00	10-Nov-26	19-Nov-26	13-May-26	06-Aug-26	0.00	28,810.00	0.00
CON-LEG101-LR-2530	Installation of Fire Hydrant [Local – 06]	15	42,210.00	21-Nov-26	07-Dec-26	10-Jun-26	03-Sep-26	0.00	42,210.00	0.00
Public Water Utility Distribution		30	119,324.80	10-Nov-26	18-Jan-27	01-Apr-26	19-May-26	0.00	119,324.80	0.00
Pipe Work		30	107,264.80	10-Nov-26	18-Jan-27	01-Apr-26	19-May-26	0.00	107,264.80	0.00
CON-LEG101-LR-10110	Excavation for Public Water Utility Distribution Piping [Local – 06]	11	20,551.50	10-Nov-26	22-Nov-26	01-Apr-26	12-Apr-26	0.00	20,551.50	0.00
CON-LEG101-LR-10210	Granular bedding for Public Water Utility Distribution Piping [Local – 06	8	5,138.10	23-Nov-26	01-Dec-26	13-Apr-26	09-May-26	0.00	5,138.10	0.00
CON-LEG101-LR-10310	Installation of Pipe for Public Water Utility Distribution Piping [Local – 0	12	46,243.80	02-Dec-26	15-Dec-26	15-Apr-26	10-May-26	0.00	46,243.80	0.00
CON-LEG101-LR-10410	Testing for Public Water Utility Distribution Piping [Local – 06]	8	10,277.10	16-Dec-26	24-Dec-26	11-May-26	12-May-26	0.00	10,277.10	0.00
CON-LEG101-LR-10510	Concrete encasement, pipe dia 110 mm [Local – 06]	3	4,501.00	26-Dec-26	28-Dec-26	13-May-26	14-May-26	0.00	4,501.00	0.00
CON-LEG101-LR-10610	Granular Surround for Public Water Utility Distribution Piping [Local – 0	8	5,138.10	29-Dec-26	06-Jan-27	13-May-26	14-May-26	0.00	5,138.10	0.00
CON-LEG101-LR-10710	Installation of Micron Marker Magnetic Tape [Local – 06]	3	5,138.10	07-Jan-27	10-Jan-27	16-May-26	16-May-26	0.00	5,138.10	0.00
CON-LEG101-LR-10810	Backfilling to Subgrade Elevation [Local – 06]	7	10,277.10	11-Jan-27	18-Jan-27	17-May-26	19-May-26	0.00	10,277.10	0.00
Valves/Chamber		3	12,060.00	11-Jan-27	13-Jan-27	09-May-26	10-May-26	0.00	12,060.00	0.00
CON-LEG101-LR-1070	Installation of Gate (Sluice) valves (Direct buried) [Local – 06]	3	12,060.00	11-Jan-27	13-Jan-27	09-May-26	10-May-26	0.00	12,060.00	0.00
Electrical Works		36	92,027.80	19-Jan-27	06-Feb-27	13-Jun-26	02-Aug-26	0.00	92,027.80	0.00
Low Voltage		36	92,027.80	19-Jan-27	06-Feb-27	13-Jun-26	02-Aug-26	0.00	92,027.80	0.00
CON-LEG101-LR-8050	Installation of Low Voltage Cables Duct Banks [Local – 06]	4	9,045.00	26-Jan-27	30-Jan-27	13-Jun-26	17-Jun-26	0.00	9,045.00	0.00
CON-LEG101-LR-7850	Excavation works for Low Voltage Cables [Local – 06]	6	0.00	19-Jan-27	25-Jan-27	23-Jul-26	30-Jul-26	0.00	0.00	0.00
CON-LEG101-LR-7950	Installation of Low Voltage Cables [Local – 06]	6	82,982.80	31-Jan-27	06-Feb-27	25-Jul-26	02-Aug-26	0.00	82,982.80	0.00
Telecommunications		51	158,270.40	07-Feb-27	17-Mar-27	13-May-26		0.00	154,837.10	0.00
CON-LEG101-LR-9000	Installation of Concrete encased duct banks for primary network [Local	6	29,551.50	16-Feb-27	23-Feb-27	13-Jun-26	17-Jun-26	0.00	29,551.50	0.00
CON-LEG101-LR-9300	Installation of Concrete encased duct banks for for combined network (	4	1,008.00	07-Mar-27	10-Mar-27	13-Jun-26	17-Jun-26	0.00	1,008.00	0.00
CON-LEG101-LR-8900	Installation of Sand and soil encased duct banks for primary network [L	4	64,984.40	07-Feb-27	15-Feb-27	13-Jun-26	04-Jul-26	0.00	64,984.40	0.00
CON-LEG101-LR-9400	Installation of Reinforced concrete manhole [Local – 06]	6	45,560.00	11-Mar-27	17-Mar-27	13-May-26	05-Jul-26	0.00	45,560.00	0.00
CON-LEG101-LR-9100	Installation of Sand encased duct banks for secondary network [Local –	5	13,851.00	24-Feb-27	01-Mar-27	24-Aug-26		0.00	11,080.80	0.00
CON-LEG101-LR-9200	Installation of Sand and soil encased duct banks, for combined network	4	3,315.50	02-Mar-27	06-Mar-27	24-Aug-26		0.00	2,652.40	0.00
CCTV feeding system and GSM		27	117,250.00	16-Feb-27	14-Mar-27	06-Jun-26		0.00	114,235.00	0.00
CON-LEG101-LR-9920	Installation of 25 Meters pole for CCTV Cameras [Local – 06]	4	87,100.00	06-Mar-27	09-Mar-27	06-Jun-26	12-Jul-26	0.00	87,100.00	0.00
CON-LEG101-LR-9510	Installation of 8POE ports Industrial Switches for remote poles [Local –	7	0.00	16-Feb-27	24-Feb-27	20-Jul-26		0.00	0.00	0.00
CON-LEG101-LR-9680	Installation of IP Outdoor CCTV POE Camera,5 MP, Metal Housing [Loca	4	6,700.00	25-Feb-27	01-Mar-27	20-Jul-26		0.00	6,030.00	0.00
CON-LEG101-LR-9760	Installation of Outdoor PTZ IP66 [Local – 06]	3	23,450.00	02-Mar-27	04-Mar-27	20-Jul-26		0.00	21,105.00	0.00
CON-LEG101-LR-10010	Installation of Short Range wireless point to point wireless bridge [Loca	4	0.00	10-Mar-27	14-Mar-27	20-Jul-26		0.00	0.00	0.00
Earthing System		3	0.00	16-Mar-27	18-Mar-27			0.00	0.00	0.00

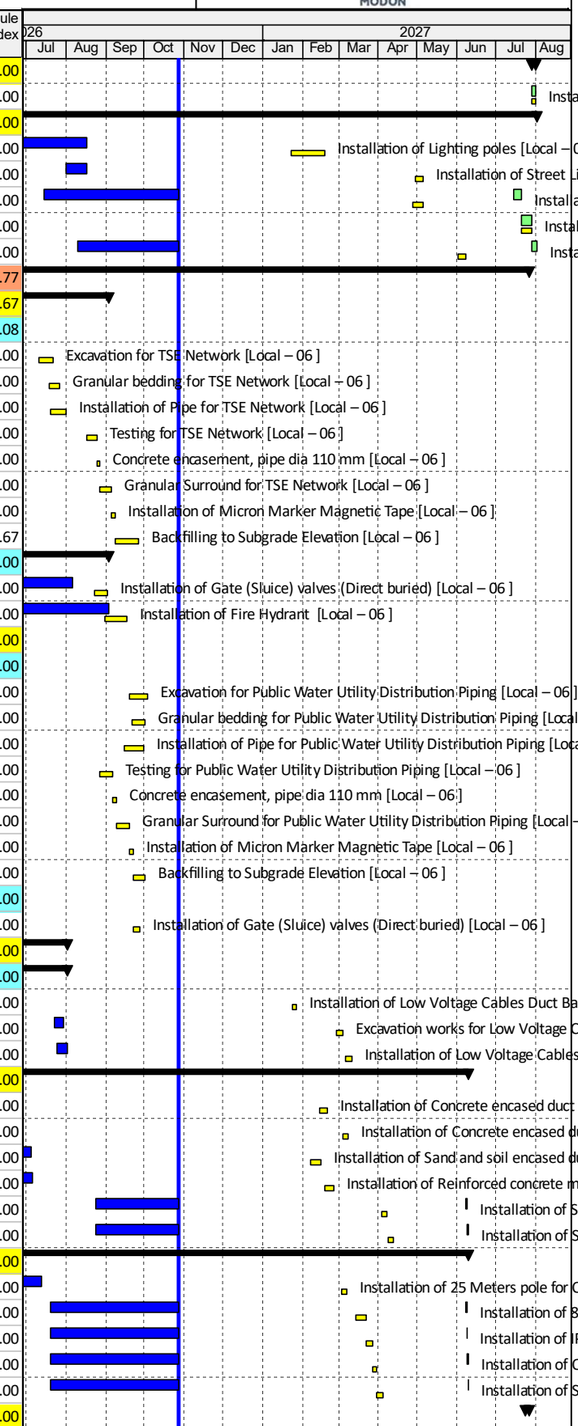


© Oracle Corporation

Activity ID	Activity Name	Original Duration	Budgeted Total Cost	BL Project Start	BL Project Finish	Actual Start	Actual Finish	Planned Value Cost	Earned Value Cost	Schedule Performance Index
CON-LEG101-LR-15140	Installation of Earthing for Distribution panels,SL feeder pillars, KWH, U	3	0.00	16-Mar-27	18-Mar-27			0.00	0.00	0.00
Road Lighting		127	132,660.00	23-Feb-27	18-Mar-27	16-Mar-26		0.00	132,660.00	0.00
CON-LEG101-LR-8150	Installation of Lighting poles [Local – 06]	10	102,510.00	23-Feb-27	06-Mar-27	16-Mar-26	17-Aug-26	0.00	102,510.00	0.00
CON-LEG101-LR-8250	Installation of Street Lighting Luminaire [Local – 06]	4	30,150.00	07-Mar-27	10-Mar-27	22-Jul-26	17-Aug-26	0.00	30,150.00	0.00
CON-LEG101-LR-7470	Installation of Unit Substation Including concrete foundations and fencir	4	0.00	07-Mar-27	10-Mar-27	11-Jul-26		0.00	0.00	0.00
CON-LEG101-LR-7550	Installation of Ring Main Unit RMU [Local – 06]	4	0.00	11-Mar-27	15-Mar-27			0.00	0.00	0.00
CON-LEG101-LR-8400	Installation of Earthing for Streetlighting feeders for every end pole circ	3	0.00	16-Mar-27	18-Mar-27	12-Aug-26		0.00	0.00	0.00
Local – 07		260	451,553.05	08-Dec-26	18-Mar-27	03-Feb-26		0.00	357,753.05	0.00
TSE Network		101	94,742.90	08-Dec-26	02-Mar-27	03-Feb-26	05-Sep-26	0.00	94,742.90	0.00
Pipe Work		48	65,262.90	08-Dec-26	10-Jan-27	03-Feb-26	31-May-26	0.00	65,262.90	0.00
CON-LEG101-LR-1390	Excavation for TSE Network [Local – 07]	7	13,047.30	08-Dec-26	15-Dec-26	03-Feb-26	09-Feb-26	0.00	13,047.30	0.00
CON-LEG101-LR-1500	Granular bedding for TSE Network [Local – 07]	2	3,265.50	16-Dec-26	17-Dec-26	10-Feb-26	19-Feb-26	0.00	3,265.50	0.00
CON-LEG101-LR-1610	Installation of Pipe for TSE Network [Local – 07]	7	29,366.10	19-Dec-26	26-Dec-26	11-Feb-26	21-Feb-26	0.00	29,366.10	0.00
CON-LEG101-LR-1940	Granular Surround for TSE Network [Local – 07]	2	3,265.50	31-Dec-26	02-Jan-27	21-Feb-26	22-Feb-26	0.00	3,265.50	0.00
CON-LEG101-LR-2050	Installation of Micron Marker Magnetic Tape [Local – 07]	3	3,265.50	03-Jan-27	05-Jan-27	24-Mar-26	24-Mar-26	0.00	3,265.50	0.00
CON-LEG101-LR-2160	Backfilling to Subgrade Elevation [Local – 07]	4	6,526.50	06-Jan-27	10-Jan-27	25-Mar-26	26-Mar-26	0.00	6,526.50	0.00
CON-LEG101-LR-1720	Testing for TSE Network [Local – 07]	4	6,526.50	27-Dec-26	30-Dec-26	31-May-26	31-May-26	0.00	6,526.50	0.00
Valves/Chamber		16	29,480.00	27-Jan-27	02-Mar-27	03-May-26	05-Sep-26	0.00	29,480.00	0.00
CON-LEG101-LR-2270	Installation of Gate (Sluice) valves (Direct buried) [Local – 07]	10	17,420.00	27-Jan-27	07-Feb-27	03-May-26	15-Jul-26	0.00	17,420.00	0.00
CON-LEG101-LR-2540	Installation of Fire Hydrant [Local – 07]	15	12,060.00	08-Feb-27	02-Mar-27	03-Jun-26	05-Sep-26	0.00	12,060.00	0.00
Public Water Utility Distribution		109	51,018.10	19-Jan-27	18-Mar-27	03-Feb-26	06-Aug-26	0.00	51,018.10	0.00
Pipe Work		76	44,988.10	19-Jan-27	13-Mar-27	03-Feb-26	14-May-26	0.00	44,988.10	0.00
CON-LEG101-LR-10120	Excavation for Public Water Utility Distribution Piping [Local – 07]	10	7,192.80	19-Jan-27	30-Jan-27	03-Feb-26	09-Feb-26	0.00	7,192.80	0.00
CON-LEG101-LR-10220	Granular bedding for Public Water Utility Distribution Piping [Local – 07	4	1,800.00	31-Jan-27	03-Feb-27	10-Feb-26	19-Feb-26	0.00	1,800.00	0.00
CON-LEG101-LR-10320	Installation of Pipe for Public Water Utility Distribution Piping [Local – 0	10	16,184.70	04-Feb-27	20-Feb-27	11-Feb-26	21-Feb-26	0.00	16,184.70	0.00
CON-LEG101-LR-10620	Granular Surround for Public Water Utility Distribution Piping [Local – 0	3	1,800.00	04-Mar-27	07-Mar-27	21-Feb-26	22-Feb-26	0.00	1,800.00	0.00
CON-LEG101-LR-10520	Concrete encasement, pipe dia 110 mm [Local – 07]	6	9,016.00	25-Feb-27	03-Mar-27	17-Mar-26	17-Mar-26	0.00	9,016.00	0.00
CON-LEG101-LR-10720	Installation of Micron Marker Magnetic Tape [Local – 07]	3	1,800.00	08-Mar-27	10-Mar-27	24-Mar-26	24-Mar-26	0.00	1,800.00	0.00
CON-LEG101-LR-10820	Backfilling to Subgrade Elevation [Local – 07]	2	3,597.30	11-Mar-27	13-Mar-27	25-Mar-26	26-Mar-26	0.00	3,597.30	0.00
CON-LEG101-LR-10420	Testing for Public Water Utility Distribution Piping [Local – 07]	3	3,597.30	21-Feb-27	24-Feb-27	13-May-26	14-May-26	0.00	3,597.30	0.00
Valves/Chamber		5	6,030.00	14-Mar-27	18-Mar-27	03-May-26	06-Aug-26	0.00	6,030.00	0.00
CON-LEG101-LR-1080	Installation of Gate (Sluice) valves (Direct buried) [Local – 07]	5	6,030.00	14-Mar-27	18-Mar-27	03-May-26	06-Aug-26	0.00	6,030.00	0.00
Electrical Works		41	23,011.10	31-Jan-27	24-Feb-27	01-Jun-26	27-Jul-26	0.00	23,011.10	0.00
Low Voltage		41	23,011.10	31-Jan-27	24-Feb-27	01-Jun-26	27-Jul-26	0.00	23,011.10	0.00
CON-LEG101-LR-8060	Installation of Low Voltage Cables Duct Banks [Local – 07]	3	2,264.50	08-Feb-27	15-Feb-27	01-Jun-26	03-Jun-26	0.00	2,264.50	0.00
CON-LEG101-LR-7860	Excavation works for Low Voltage Cables [Local – 07]	7	0.00	31-Jan-27	07-Feb-27	22-Jul-26	25-Jul-26	0.00	0.00	0.00
CON-LEG101-LR-7960	Installation of Low Voltage Cables [Local – 07]	7	20,746.60	16-Feb-27	24-Feb-27	25-Jul-26	27-Jul-26	0.00	20,746.60	0.00
Telecommunications		40	73,740.95	20-Feb-27	14-Mar-27	20-May-26	10-Sep-26	0.00	73,740.95	0.00
CON-LEG101-LR-9310	Installation of Concrete encased duct banks for for combined network	2	252.00	08-Mar-27	09-Mar-27	20-May-26	24-May-26	0.00	252.00	0.00
CON-LEG101-LR-9410	Installation of Reinforced concrete manhole [Local – 07]	4	45,560.00	10-Mar-27	14-Mar-27	20-May-26	06-Jul-26	0.00	45,560.00	0.00
CON-LEG101-LR-8910	Installation of Sand and soil encased duct banks for primary network [L	4	16,248.70	20-Feb-27	24-Feb-27	08-Aug-26	10-Sep-26	0.00	16,248.70	0.00
CON-LEG101-LR-9010	Installation of Concrete encased duct banks for primary network [Local	2	7,388.25	25-Feb-27	27-Feb-27	08-Aug-26	10-Sep-26	0.00	7,388.25	0.00
CON-LEG101-LR-9110	Installation of Sand encased duct banks for secondary network [Local –	3	3,463.00	28-Feb-27	02-Mar-27	08-Aug-26	10-Sep-26	0.00	3,463.00	0.00
CON-LEG101-LR-9210	Installation of Sand and soil encased duct banks, for combined network	4	829.00	03-Mar-27	07-Mar-27	08-Aug-26	10-Sep-26	0.00	829.00	0.00
CCTV feeding system and GSM		7	0.00	25-Feb-27	04-Mar-27	22-Jul-26		0.00	0.00	0.00
CON-LEG101-LR-10020	Installation of Short Range wireless point to point wireless bridge [Loca	7	0.00	25-Feb-27	04-Mar-27	22-Jul-26		0.00	0.00	0.00
Earthing System		4	5,360.00	15-Mar-27	18-Mar-27			0.00	0.00	0.00
CON-LEG101-LR-15130	Installation of Earthing for Distribution panels,SL feeder pillars, KWH, U	4	5,360.00	15-Mar-27	18-Mar-27			0.00	0.00	0.00
Road Lighting		113	203,680.00	23-Feb-27	18-Mar-27	17-May-26		0.00	115,240.00	0.00
CON-LEG101-LR-8160	Installation of Lighting poles [Local – 07]	7	68,340.00	23-Feb-27	02-Mar-27	17-May-26	17-Aug-26	0.00	68,340.00	0.00
CON-LEG101-LR-8260	Installation of Street Lighting Luminaire [Local – 07]	7	20,100.00	03-Mar-27	10-Mar-27	18-Jul-26	17-Aug-26	0.00	20,100.00	0.00
CON-LEG101-LR-7480	Installation of Unit Substation Including concrete foundations and fencir	4	56,950.00	06-Mar-27	09-Mar-27	12-Jul-26		0.00	22,780.00	0.00
CON-LEG101-LR-7560	Installation of Ring Main Unit RMU [Local – 07]	4	50,250.00	10-Mar-27	14-Mar-27			0.00	0.00	0.00

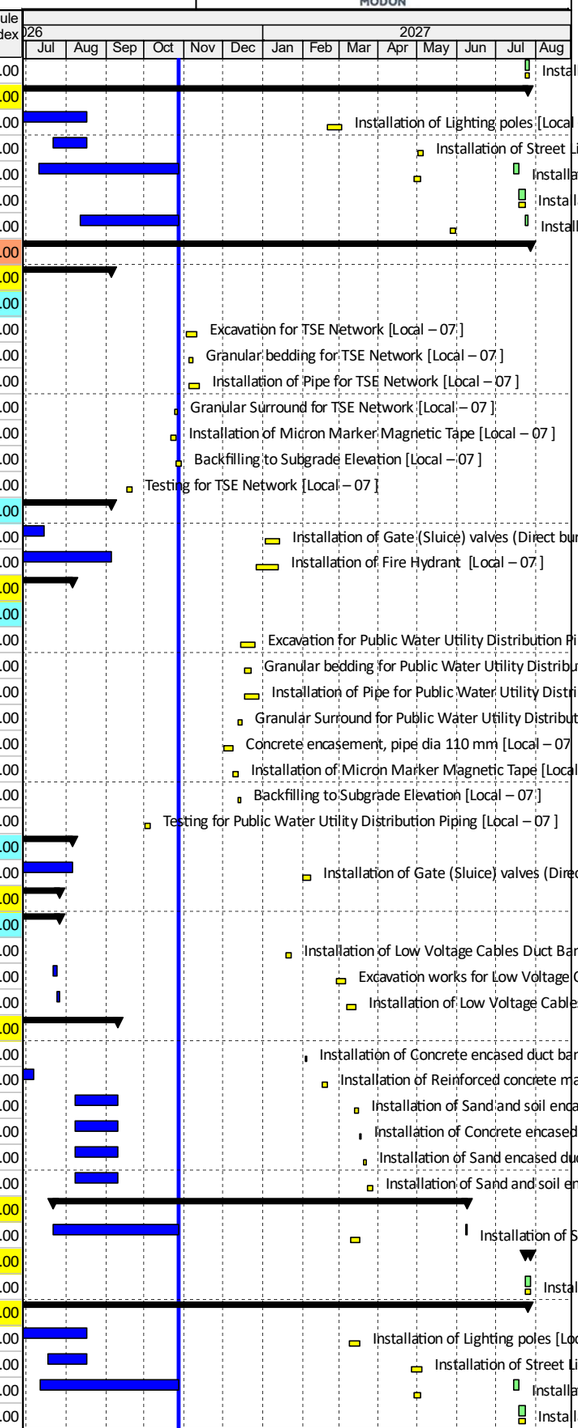


© Oracle Corporation

Activity ID	Activity Name	Original Duration	Budgeted Total Cost	BL Project Start	BL Project Finish	Actual Start	Actual Finish	Planned Value Cost	Earned Value Cost	Schedule Performance Index
CON-LEG101-LR-8410	Installation of Earthing for Streetlighting feeders for every end pole circ	4	8,040.00	15-Mar-27	18-Mar-27	26-Aug-26		0.00	4,020.00	0.00
Local – 08		344	1,033,614.65	11-Aug-26	18-Mar-27	19-Jan-26		175,823.66	885,209.65	5.03
TSE Network		113	369,622.60	11-Aug-26	18-Mar-27	19-Jan-26		175,823.66	365,602.60	2.08
Pipe Work		66	186,712.60	11-Aug-26	08-Nov-26	19-Jan-26	16-Apr-26	175,823.66	186,712.60	1.06
CON-LEG101-LR-1400	Excavation for TSE Network [Local – 08]	11	37,019.10	11-Aug-26	23-Aug-26	19-Jan-26	25-Jan-26	37,019.10	37,019.10	1.00
CON-LEG101-LR-1510	Granular bedding for TSE Network [Local – 08]	9	9,256.20	24-Aug-26	02-Sep-26	26-Jan-26	11-Feb-26	9,256.20	9,256.20	1.00
CON-LEG101-LR-1620	Installation of Pipe for TSE Network [Local – 08]	15	83,299.50	03-Sep-26	20-Sep-26	27-Jan-26	18-Feb-26	83,299.50	83,299.50	1.00
CON-LEG101-LR-1950	Granular Surround for TSE Network [Local – 08]	9	9,256.20	05-Oct-26	14-Oct-26	29-Jan-26	19-Feb-26	9,256.20	9,256.20	1.00
CON-LEG101-LR-1840	Concrete encasement, pipe dia 110 mm [Local – 08]	2	1,603.00	03-Oct-26	04-Oct-26	11-Feb-26	21-Feb-26	1,603.00	1,603.00	1.00
CON-LEG101-LR-2060	Installation of Micron Marker Magnetic Tape [Local – 08]	4	9,256.20	15-Oct-26	19-Oct-26	21-Feb-26	22-Feb-26	9,256.20	9,256.20	1.00
CON-LEG101-LR-2170	Backfilling to Subgrade Elevation [Local – 08]	17	18,511.20	20-Oct-26	08-Nov-26	22-Feb-26	23-Feb-26	7,622.26	18,511.20	2.43
CON-LEG101-LR-1730	Testing for TSE Network [Local – 08]	9	18,511.20	21-Sep-26	01-Oct-26	15-Apr-26	16-Apr-26	18,511.20	18,511.20	1.00
Valves/Chamber		107	182,910.00	09-Nov-26	18-Mar-27	04-Mar-26		0.00	178,890.00	0.00
CON-LEG101-LR-2280	Installation of Gate (Sluice) valves (Direct buried) [Local – 08]	14	28,140.00	28-Dec-26	12-Jan-27	04-Mar-26	06-Aug-26	0.00	28,140.00	0.00
CON-LEG101-LR-2370	Installation of Wash-out Valves [Local – 08]	15	8,040.00	13-Jan-27	30-Jan-27	04-Mar-26	06-Aug-26	0.00	8,040.00	0.00
CON-LEG101-LR-2450	Installation of Air Valves [Local – 08]	15	12,060.00	31-Jan-27	21-Feb-27	04-Mar-26	06-Aug-26	0.00	12,060.00	0.00
CON-LEG101-LR-2550	Installation of Fire Hydrant [Local – 08]	21	54,270.00	23-Feb-27	18-Mar-27	05-Mar-26	30-Sep-26	0.00	54,270.00	0.00
CON-LEG101-LR-2670	Installation of Wash out chambers [Local – 08]	21	53,600.00	09-Nov-26	02-Dec-26	30-Apr-26		0.00	50,920.00	0.00
CON-LEG101-LR-2750	Installation of Air Valve chambers [Local – 08]	21	26,800.00	03-Dec-26	27-Dec-26	16-Apr-26		0.00	25,460.00	0.00
Public Water Utility Distribution		199	160,430.50	09-Nov-26	18-Mar-27	07-Mar-26	06-Aug-26	0.00	160,430.50	0.00
Pipe Work		36	148,370.50	09-Nov-26	16-Jan-27	07-Mar-26	16-Apr-26	0.00	148,370.50	0.00
CON-LEG101-LR-10130	Excavation for Public Water Utility Distribution Piping [Local – 08]	11	28,774.80	09-Nov-26	21-Nov-26	07-Mar-26	10-Mar-26	0.00	28,774.80	0.00
CON-LEG101-LR-10230	Granular bedding for Public Water Utility Distribution Piping [Local – 08	8	7,192.80	22-Nov-26	30-Nov-26	11-Mar-26	14-Mar-26	0.00	7,192.80	0.00
CON-LEG101-LR-10330	Installation of Pipe for Public Water Utility Distribution Piping [Local – 0	11	64,741.50	01-Dec-26	13-Dec-26	15-Mar-26	24-Mar-26	0.00	64,741.50	0.00
CON-LEG101-LR-10530	Concrete encasement, pipe dia 110 mm [Local – 08]	3	4,501.00	23-Dec-26	26-Dec-26	26-Mar-26	26-Mar-26	0.00	4,501.00	0.00
CON-LEG101-LR-10630	Granular Surround for Public Water Utility Distribution Piping [Local – 0	8	7,192.80	27-Dec-26	04-Jan-27	28-Mar-26	28-Mar-26	0.00	7,192.80	0.00
CON-LEG101-LR-10730	Installation of Micron Marker Magnetic Tape [Local – 08]	3	7,192.80	05-Jan-27	07-Jan-27	29-Mar-26	30-Mar-26	0.00	7,192.80	0.00
CON-LEG101-LR-10830	Backfilling to Subgrade Elevation [Local – 08]	7	14,387.40	09-Jan-27	16-Jan-27	31-Mar-26	02-Apr-26	0.00	14,387.40	0.00
CON-LEG101-LR-10430	Testing for Public Water Utility Distribution Piping [Local – 08]	8	14,387.40	14-Dec-26	22-Dec-26	16-Apr-26	16-Apr-26	0.00	14,387.40	0.00
Valves/Chamber		5	12,060.00	14-Mar-27	18-Mar-27	03-May-26	06-Aug-26	0.00	12,060.00	0.00
CON-LEG101-LR-1090	Installation of Gate (Sluice) valves (Direct buried) [Local – 08]	5	12,060.00	14-Mar-27	18-Mar-27	03-May-26	06-Aug-26	0.00	12,060.00	0.00
Electrical Works		254	130,338.90	17-Jan-27	02-Mar-27	07-Jul-26		0.00	103,538.90	0.00
Low Voltage		254	130,338.90	17-Jan-27	02-Mar-27	07-Jul-26		0.00	103,538.90	0.00
CON-LEG101-LR-8070	Installation of Low Voltage Cables Duct Banks [Local – 08]	10	10,181.00	28-Jan-27	08-Feb-27	07-Jul-26	09-Jul-26	0.00	10,181.00	0.00
CON-LEG101-LR-7870	Excavation works for Low Voltage Cables [Local – 08]	10	0.00	17-Jan-27	27-Jan-27	18-Aug-26	27-Aug-26	0.00	0.00	0.00
CON-LEG101-LR-7970	Installation of Low Voltage Cables [Local – 08]	7	93,357.90	14-Feb-27	21-Feb-27	19-Aug-26	27-Aug-26	0.00	93,357.90	0.00
CON-LEG101-LR-8500	Installation of Low Voltage Distribution Panel [Local – 08]	7	26,800.00	23-Feb-27	02-Mar-27			0.00	0.00	0.00
Telecommunications		189	160,966.65	28-Jan-27	16-Mar-27	07-Jul-26	15-Oct-26	0.00	160,966.65	0.00
CON-LEG101-LR-9020	Installation of Concrete encased duct banks for primary network [Local	8	33,246.75	07-Feb-27	20-Feb-27	07-Jul-26	09-Jul-26	0.00	33,246.75	0.00
CON-LEG101-LR-9320	Installation of Concrete encased duct banks for for combined network (	5	1,132.00	04-Mar-27	09-Mar-27	07-Jul-26	09-Jul-26	0.00	1,132.00	0.00
CON-LEG101-LR-8920	Installation of Sand and soil encased duct banks for primary network [L	8	73,107.90	28-Jan-27	06-Feb-27	22-Sep-26	07-Oct-26	0.00	73,107.90	0.00
CON-LEG101-LR-9120	Installation of Sand encased duct banks for secondary network [Local –	5	15,580.00	21-Feb-27	27-Feb-27	23-Sep-26	07-Oct-26	0.00	15,580.00	0.00
CON-LEG101-LR-9220	Installation of Sand and soil encased duct banks, for combined network	4	3,730.00	28-Feb-27	03-Mar-27	24-Sep-26	07-Oct-26	0.00	3,730.00	0.00
CON-LEG101-LR-9420	Installation of Reinforced concrete manhole [Local – 08]	6	34,170.00	10-Mar-27	16-Mar-27	26-Sep-26	15-Oct-26	0.00	34,170.00	0.00
CCTV feeding system and GSM		194	0.00	07-Feb-27	11-Mar-27	05-Jul-26		0.00	0.00	0.00
CON-LEG101-LR-9930	Installation of 25 Meters pole for CCTV Cameras [Local – 08]	7	0.00	24-Feb-27	03-Mar-27	05-Jul-26	11-Jul-26	0.00	0.00	0.00
CON-LEG101-LR-9770	Installation of Outdoor PTZ IP66 [Local – 08]	3	0.00	07-Feb-27	14-Feb-27	25-Jul-26		0.00	0.00	0.00
CON-LEG101-LR-9820	Installation of LED Screen 43" (24/7 operation) with Ethernet decoders	7	0.00	15-Feb-27	23-Feb-27			0.00	0.00	0.00
CON-LEG101-LR-10030	Installation of Short Range wireless point to point wireless bridge [Loca	7	0.00	04-Mar-27	11-Mar-27	25-Jul-26		0.00	0.00	0.00
Earthing System		2	10,720.00	17-Mar-27	18-Mar-27			0.00	0.00	0.00
CON-LEG101-LR-8320	Installation of Earthing for Distribution panels,SL feeder pillars, KWH, U	2	10,720.00	17-Mar-27	18-Mar-27			0.00	0.00	0.00
Road Lighting		132	201,536.00	23-Feb-27	18-Mar-27	19-Apr-26		0.00	94,671.00	0.00
CON-LEG101-LR-8170	Installation of Lighting poles [Local – 08]	7	27,336.00	23-Feb-27	02-Mar-27	19-Apr-26	25-Oct-26	0.00	27,336.00	0.00

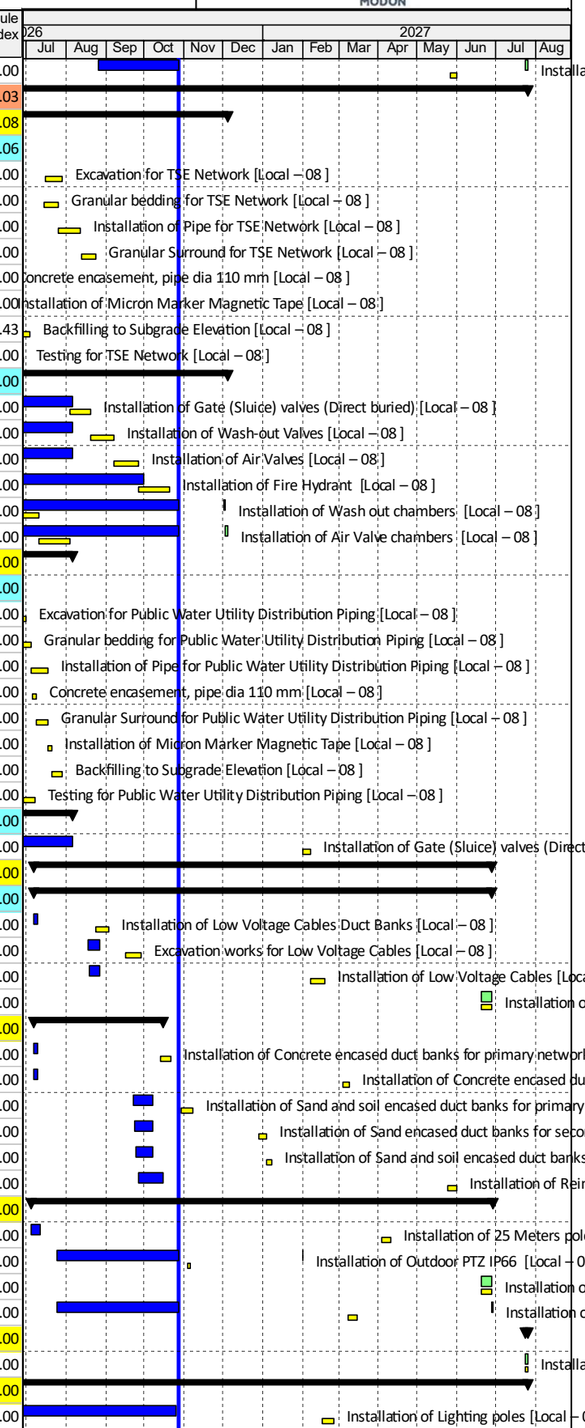


© Oracle Corporation

Activity ID	Activity Name	Original Duration	Budgeted Total Cost	BL Project Start	BL Project Finish	Actual Start	Actual Finish	Planned Value Cost	Earned Value Cost	Schedule Performance Index
CON-LEG101-LR-8270	Installation of Street Lighting Luminaire [Local – 08]	4	8,040.00	03-Mar-27	07-Mar-27	22-Aug-26	25-Oct-26	0.00	8,040.00	0.00
CON-LEG101-LR-7490	Installation of Unit Substation Including concrete foundations and fencir	4	56,950.00	03-Mar-27	07-Mar-27	18-Jul-26		0.00	17,085.00	0.00
CON-LEG101-LR-7570	Installation of Ring Main Unit RMU [Local – 08]	4	50,250.00	08-Mar-27	11-Mar-27			0.00	0.00	0.00
CON-LEG101-LR-8420	Installation of Earthing for Streetlighting feeders for every end pole circ	2	12,060.00	17-Mar-27	18-Mar-27			0.00	0.00	0.00
CON-LEG101-LR-8470	Installation of Street Lighting feeder pillars / Lighting panels [Local – 0	4	46,900.00	13-Mar-27	16-Mar-27	05-Sep-26		0.00	42,210.00	0.00
Bridge		458	2,513,306.98	04-Mar-26	01-Jun-27	17-Jan-26		1,350,589.74	1,830,342.88	1.36
Substructure		150	722,830.32	04-Mar-26	09-Aug-26	17-Jan-26	01-Aug-26	722,830.32	722,830.32	1.00
Earth Work		88	112,795.32	04-Mar-26	03-Jun-26	17-Jan-26	01-Aug-26	112,795.32	112,795.32	1.00
CON-LEG101-BR-1000	Excavation for Bridge [Bridge]	21	9,853.02	04-Mar-26	01-Apr-26	17-Jan-26	15-Feb-26	9,853.02	9,853.02	Excavation for Bridge [Bridge]
CON-LEG101-BR-1010	Parcrels Excavation for Bridge [Bridge]	21	0.00	02-Apr-26	26-Apr-26	17-Jan-26	15-Feb-26	0.00	0.00	Parcrels Excavation for Bridge [Bridge]
CON-LEG101-BR-1240	Embankments to the parcels for Bridge [Bridge]	14	0.00	14-May-26	03-Jun-26	24-Jan-26	17-Feb-26	0.00	0.00	Embankments to the parcels for Bridge [Bridge]
CON-LEG101-BR-1140	Embankments to the Bridge [Bridge]	15	102,942.30	27-Apr-26	13-May-26	17-May-26	01-Aug-26	102,942.30	102,942.30	1.00
Piling		21	434,160.00	04-Jun-26	28-Jun-26	18-Jan-26	14-Mar-26	434,160.00	434,160.00	1.00
CON-LEG101-BR-1020	Reinforced concrete Piles [Bridge]	21	434,160.00	04-Jun-26	28-Jun-26	18-Jan-26	14-Mar-26	434,160.00	434,160.00	1.00
Pile Caps & Abutments		67	175,875.00	29-Jun-26	09-Aug-26	15-Feb-26	20-May-26	175,875.00	175,875.00	1.00
CON-LEG101-BR-1030	Reinforced concrete for pile caps and abutment [Bridge]	21	135,675.00	29-Jun-26	22-Jul-26	15-Feb-26	28-Mar-26	135,675.00	135,675.00	1.00
CON-LEG101-BR-1180	Installation of Elastomeric Bearings [Bridge]	15	40,200.00	23-Jul-26	09-Aug-26	01-Mar-26	20-May-26	40,200.00	40,200.00	1.00
Superstructure		168	1,023,896.56	29-Jun-26	20-Jan-27	10-Feb-26	17-Aug-26	627,759.42	1,023,896.56	1.63
Girder		59	579,336.56	29-Jun-26	05-Oct-26	10-Feb-26	23-Jun-26	579,336.56	579,336.56	1.00
Casting		46	225,576.56	29-Jun-26	16-Aug-26	10-Feb-26	26-Apr-26	225,576.56	225,576.56	1.00
CON-LEG101-BR-1100	Steel Reinforced Work	21	59,416.56	29-Jun-26	22-Jul-26	10-Feb-26	23-Apr-26	59,416.56	59,416.56	1.00
CON-LEG101-BR-1110	Formwork and Casting	21	166,160.00	23-Jul-26	16-Aug-26	16-Mar-26	26-Apr-26	166,160.00	166,160.00	1.00
Installation		35	353,760.00	17-Aug-26	05-Oct-26	30-Apr-26	23-Jun-26	353,760.00	353,760.00	1.00
CON-LEG101-BR-1120	Prestressing Strands	21	187,600.00	17-Aug-26	09-Sep-26	30-Apr-26	18-May-26	187,600.00	187,600.00	1.00
CON-LEG101-BR-1130	Installation of Girder	21	166,160.00	10-Sep-26	05-Oct-26	21-Jun-26	23-Jun-26	166,160.00	166,160.00	1.00
Slab Casting		92	444,560.00	06-Oct-26	20-Jan-27	01-Jul-26	17-Aug-26	48,422.86	444,560.00	9.18
Top Slabs		64	219,600.00	06-Oct-26	05-Dec-26	01-Jul-26	12-Jul-26	48,422.86	219,600.00	4.54
CON-LEG101-BR-1040	Steel Reinforced Work for Top Slab	21	112,560.00	31-Oct-26	23-Nov-26	02-Jul-26	08-Jul-26	0.00	112,560.00	0.00
CON-LEG101-BR-1050	Formwork for Top Slab	21	53,520.00	06-Oct-26	29-Oct-26	01-Jul-26	09-Jul-26	48,422.86	53,520.00	1.11
CON-LEG101-BR-1060	Casting Concrete & Treatment for Top Slab	10	53,520.00	24-Nov-26	05-Dec-26	12-Jul-26	12-Jul-26	0.00	53,520.00	0.00
Apron Slabs		40	224,960.00	06-Dec-26	20-Jan-27	05-Aug-26	17-Aug-26	0.00	224,960.00	0.00
CON-LEG101-BR-1250	Lean concrete For Apron Slab [Bridge]	4	5,360.00	06-Dec-26	09-Dec-26	05-Aug-26	05-Aug-26	0.00	5,360.00	0.00
CON-LEG101-BR-1070	Steel Reinforced Work for Apron Slab	15	112,560.00	10-Dec-26	27-Dec-26	08-Aug-26	17-Aug-26	0.00	112,560.00	0.00
CON-LEG101-BR-1080	Formwork Work for Apron Slab	15	53,520.00	28-Dec-26	13-Jan-27	09-Aug-26	17-Aug-26	0.00	53,520.00	0.00
CON-LEG101-BR-1090	Casting Concrete Work & Treatment for Apron Slab	6	53,520.00	14-Jan-27	20-Jan-27	11-Aug-26	17-Aug-26	0.00	53,520.00	0.00
Bridge Finishing		255	750,500.10	26-Jan-27	01-Jun-27	13-Jul-26		0.00	67,536.00	0.00
CON-LEG101-BR-1150	Installation of New Jersey [Bridge]	20	32,160.00	26-Jan-27	23-Feb-27	13-Jul-26	06-Aug-26	0.00	32,160.00	0.00
CON-LEG101-BR-1270	Installation of Lighting poles [Bridge]	18	35,376.00	03-Mar-27	23-Mar-27	23-Sep-26	26-Sep-26	0.00	35,376.00	0.00
CON-LEG101-BR-1260	Asphalt Wearing Cource	3	49,974.00	23-Mar-27	25-Mar-27			0.00	0.00	0.00
CON-LEG101-BR-1160	Membrane waterproofing for concert in touch with soil and membrar	10	40,200.00	24-Feb-27	07-Mar-27			0.00	0.00	0.00
CON-LEG101-BR-1170	Placing of Protective Coating for Concrete Surfaces [Bridge]	13	61,070.10	08-Mar-27	22-Mar-27			0.00	0.00	0.00
CON-LEG101-BR-1190	Installation of expansion joints for bridges [Bridge]	14	76,120.00	27-Mar-27	11-Apr-27			0.00	0.00	0.00
CON-LEG101-BR-1200	Installation of Guard Rail [Bridge]	20	96,480.00	12-Apr-27	04-May-27			0.00	0.00	0.00
CON-LEG101-BR-1210	Installation of GRP Panel [Bridge]	10	251,920.00	05-May-27	20-May-27			0.00	0.00	0.00
CON-LEG101-BR-1220	Installation of Logo MODON [Bridge]	10	107,200.00	22-May-27	01-Jun-27			0.00	0.00	0.00
Drainage		10	16,080.00	14-Jan-27	25-Jan-27	09-Jul-26	11-Jul-26	0.00	16,080.00	0.00
Gully Installation		10	16,080.00	14-Jan-27	25-Jan-27	09-Jul-26	11-Jul-26	0.00	16,080.00	0.00
CON-LEG101-BR-1230	Installation of Bridge Gully (Scupper) drainage units [Bridge]	10	16,080.00	14-Jan-27	25-Jan-27	09-Jul-26	11-Jul-26	0.00	16,080.00	0.00
Outside Boundary Area (Tie-in Lines)		419	2,681,726.27	01-Jan-26	04-May-27	05-Jan-26		1,472,114.02	2,663,147.17	1.81
Permits & Prepation works for Construction		84	0.00	01-Jan-26	14-Apr-26	05-Jan-26	16-Apr-26	0.00	0.00	0.00
CON-LEG101-OBA-1230	Permits for Starting Works	20	0.00	01-Jan-26	24-Jan-26	05-Jan-26	12-Feb-26	0.00	0.00	Permits for Starting Works 0.00
CON-LEG101-OBA-1240	As Built for Existing Utilites	21	0.00	25-Jan-26	17-Feb-26	07-Jan-26	14-Feb-26	0.00	0.00	As Built for Existing Utilites 0.00
CON-LEG101-OBA-1250	Submission of Engineering Works	21	0.00	18-Feb-26	15-Mar-26	15-Feb-26	09-Apr-26	0.00	0.00	0.00 Engineering Works

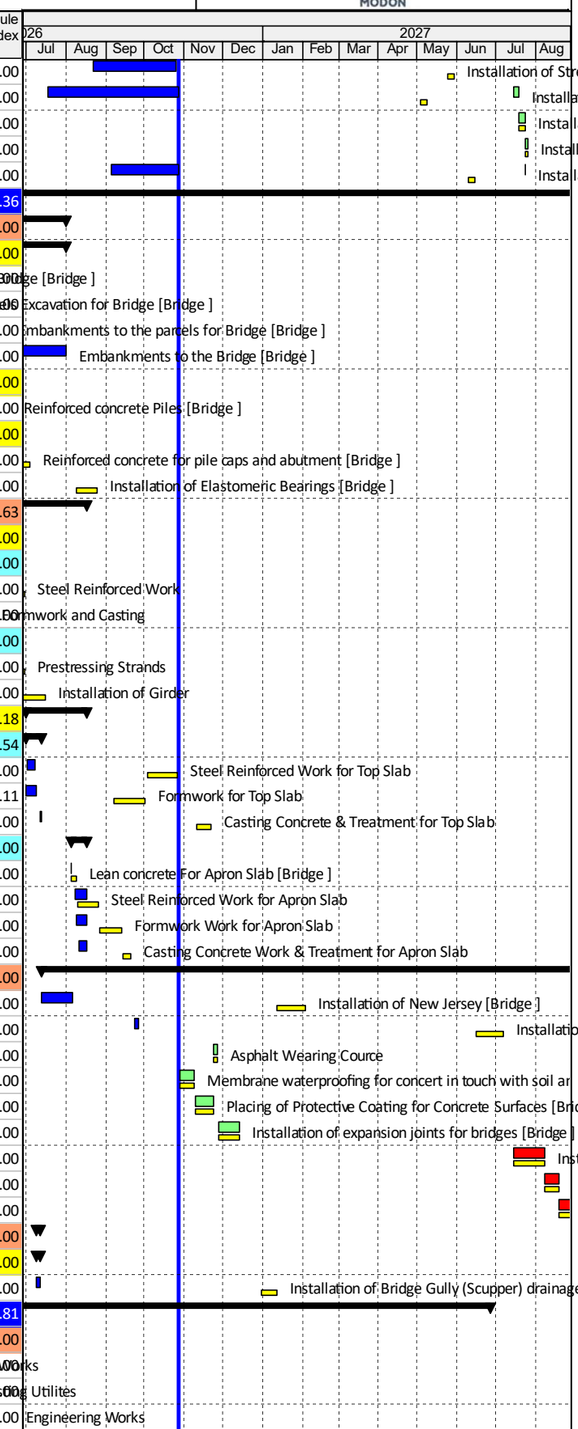


© Oracle Corporation

Activity ID	Activity Name	Original Duration	Budgeted Total Cost	BL Project Start	BL Project Finish	Actual Start	Actual Finish	Planned Value Cost	Earned Value Cost	Schedule Performance Index
CON-LEG101-OBA-1260	Approval of Engineering Works	12	0.00	16-Mar-26	02-Apr-26	19-Feb-26	15-Apr-26	0.00	0.00	0.00
CON-LEG101-OBA-1270	Detour & Safety works	10	0.00	04-Apr-26	14-Apr-26	12-Feb-26	16-Apr-26	0.00	0.00	0.00
Sanitary Sewerage		145	779,947.00	15-Apr-26	06-Oct-26	14-Feb-26		779,947.00	771,404.50	0.99
Pipe Work		99	609,097.00	15-Apr-26	10-Sep-26	14-Feb-26	11-May-26	609,097.00	609,097.00	1.00
CON-LEG101-OBA-1080	Excavation for Sanitary Sewerage Network [Outside Boundary Area]	21	121,817.50	15-Apr-26	09-May-26	14-Feb-26	03-May-26	121,817.50	121,817.50	1.00
CON-LEG101-OBA-1090	Granular bedding for Sanitary Sewerage Network [Outside Boundary	18	30,452.00	10-May-26	03-Jun-26	15-Feb-26	04-May-26	30,452.00	30,452.00	1.00
CON-LEG101-OBA-1100	Installation of Pipe for Sanitary Sewerage Network [Outside Boundary A	21	274,096.50	04-Jun-26	28-Jun-26	16-Feb-26	06-May-26	274,096.50	274,096.50	1.00
CON-LEG101-OBA-1110	Testing for Sanitary Sewerage Network [Outside Boundary Area]	21	60,913.50	29-Jun-26	22-Jul-26	10-Mar-26	07-May-26	60,913.50	60,913.50	1.00
CON-LEG101-OBA-1120	Granular Surround for Sanitary Sewerage Network [Outside Boundary	18	30,452.00	23-Jul-26	12-Aug-26	16-Feb-26	09-May-26	30,452.00	30,452.00	1.00
CON-LEG101-OBA-1130	Installation of Micron Marker Magnetic Tape [Outside Boundary Area]	7	30,452.00	13-Aug-26	20-Aug-26	11-Mar-26	10-May-26	30,452.00	30,452.00	1.00
CON-LEG101-OBA-1140	Backfilling to Subgrade Elevation [Outside Boundary Area]	18	60,913.50	22-Aug-26	10-Sep-26	12-Mar-26	11-May-26	60,913.50	60,913.50	1.00
Manhole		21	170,850.00	12-Sep-26	06-Oct-26	14-Feb-26		170,850.00	162,307.50	0.95
CON-LEG101-OBA-1150	Installation of Fiberglass Manholes [Outside Boundary Area]	21	170,850.00	12-Sep-26	06-Oct-26	14-Feb-26		170,850.00	162,307.50	0.95
TSE Network		77	655,126.00	10-Oct-26	22-Dec-26	05-May-26		58,393.75	650,516.40	11.14
Pipe Work		77	424,646.00	10-Oct-26	21-Dec-26	05-May-26	02-Jul-26	58,393.75	424,646.00	7.27
CON-LEG101-OBA-1000	Excavation for TSE Network [Outside Boundary Area]	10	42,475.00	10-Oct-26	20-Oct-26	05-May-26	16-Jun-26	42,475.00	42,475.00	1.00
CON-LEG101-OBA-1010	Granular bedding for TSE Network [Outside Boundary Area]	8	21,225.00	21-Oct-26	29-Oct-26	07-May-26	17-Jun-26	15,918.75	21,225.00	1.33
CON-LEG101-OBA-1020	Installation of Pipe for TSE Network [Outside Boundary Area]	11	21,225.00	31-Oct-26	11-Nov-26	09-May-26	18-Jun-26	0.00	21,225.00	0.00
CON-LEG101-OBA-1040	Granular Surround for TSE Network [Outside Boundary Area]	8	84,930.00	22-Nov-26	30-Nov-26	20-May-26	20-Jun-26	0.00	84,930.00	0.00
CON-LEG101-OBA-1050	Installation of Micron Marker Magnetic Tape [Outside Boundary Area]	3	21,225.00	01-Dec-26	03-Dec-26	21-May-26	21-Jun-26	0.00	21,225.00	0.00
CON-LEG101-OBA-1060	Backfilling to Subgrade Elevation [Outside Boundary Area]	15	191,091.00	05-Dec-26	21-Dec-26	24-May-26	22-Jun-26	0.00	191,091.00	0.00
CON-LEG101-OBA-1030	Testing for TSE Network [Outside Boundary Area]	8	42,475.00	12-Nov-26	21-Nov-26	01-Jul-26	02-Jul-26	0.00	42,475.00	0.00
Valves/Chamber		16	230,480.00	05-Dec-26	22-Dec-26	13-Jun-26		0.00	225,870.40	0.00
CON-LEG101-OBA-1500	Installation of Valve Chamber [Outside Boundary Area]	10	136,680.00	05-Dec-26	15-Dec-26	13-Jun-26		0.00	133,946.40	0.00
CON-LEG101-OBA-1070	Installation of Butterfly valves (In Chamber) [Outside Boundary Area]	6	93,800.00	16-Dec-26	22-Dec-26	13-Jun-26		0.00	91,924.00	0.00
Public Water Utility Distribution		326	1,246,653.27	15-Apr-26	04-May-27	01-Apr-26		633,773.27	1,241,226.27	1.96
Public Water Utility Distribution (0 - 900) m		82	415,548.73	15-Apr-26	04-Aug-26	06-May-26		415,548.73	412,533.73	0.99
Pipe Work		75	355,248.73	15-Apr-26	04-Aug-26	06-May-26	23-Jul-26	355,248.73	355,248.73	1.00
CON-LEG101-OBA-1160	Excavation for Public Water Utility Distribution Piping [Outside Boundar	21	71,048.67	15-Apr-26	09-May-26	06-May-26	18-Jun-26	71,048.67	71,048.67	1.00
CON-LEG101-OBA-1170	Granular bedding for Public Water Utility Distribution Piping [Outside B	13	17,768.07	10-May-26	24-May-26	10-May-26	27-Jun-26	17,768.07	17,768.07	1.00
CON-LEG101-OBA-1180	Installation of Pipe for Public Water Utility Distribution Piping [Outside	19	159,863.87	25-May-26	20-Jun-26	12-May-26	28-Jun-26	159,863.87	159,863.87	1.00
CON-LEG101-OBA-1200	Granular Surround for Public Water Utility Distribution Piping [Outside E	13	17,762.27	06-Jul-26	20-Jul-26	04-Jul-26	05-Jul-26	17,762.27	17,762.27	1.00
CON-LEG101-OBA-1210	Installation of Micron Marker Magnetic Tape [Outside Boundary Area]	3	17,762.27	21-Jul-26	23-Jul-26	06-Jul-26	07-Jul-26	17,762.27	17,762.27	1.00
CON-LEG101-OBA-1220	Backfilling to Subgrade Elevation [Outside Boundary Area] 0 - 900 m	10	35,517.13	25-Jul-26	04-Aug-26	08-Jul-26	09-Jul-26	35,517.13	35,517.13	1.00
CON-LEG101-OBA-1190	Testing for Public Water Utility Distribution Piping [Outside Boundary Ar	13	35,526.47	21-Jun-26	05-Jul-26	22-Jul-26	23-Jul-26	35,526.47	35,526.47	1.00
Valves/Chamber		30	60,300.00	21-Jun-26	26-Jul-26	07-Jun-26		60,300.00	57,285.00	0.95
CON-LEG101-OBA-1430	Installation of Air Valves [Outside Boundary Area] 0 - 900 m	10	10,050.00	15-Jul-26	26-Jul-26	07-Jun-26		10,050.00	9,547.50	0.95
CON-LEG101-OBA-1420	Installation of Air Valve chambers [Outside Boundary Area] 0 - 900 m	21	50,250.00	21-Jun-26	14-Jul-26	07-Jun-26		50,250.00	47,737.50	0.95
Public Water Utility Distribution (901 - 1800) m		75	475,852.27	05-Aug-26	23-Dec-26	01-Apr-26		218,224.54	473,440.27	2.17
CON-LEG101-OBA-1460	Permits for Starting Works for Area 901 - 1800 m	12	0.00	05-Aug-26	18-Aug-26	01-Apr-26	01-Apr-26	0.00	0.00	0.00
CON-LEG101-OBA-1470	Detour & Safety works for Area 901 - 1800 m	8	0.00	19-Aug-26	27-Aug-26	02-Apr-26	04-Apr-26	0.00	0.00	0.00
Pipe Work		73	355,252.27	29-Aug-26	16-Dec-26	05-Apr-26	06-Sep-26	218,224.54	355,252.27	1.63
CON-LEG101-OBA-1280	Excavation for Public Water Utility Distribution Piping [Outside Boundar	21	71,048.67	29-Aug-26	21-Sep-26	05-Apr-26	05-May-26	71,048.67	71,048.67	1.00
CON-LEG101-OBA-1290	Granular bedding for Public Water Utility Distribution Piping [Outside B	13	17,762.27	22-Sep-26	07-Oct-26	21-Apr-26	10-May-26	17,762.27	17,762.27	1.00
CON-LEG101-OBA-1300	Installation of Pipe for Public Water Utility Distribution Piping [Outside	21	159,863.87	08-Oct-26	01-Nov-26	23-Apr-26	12-May-26	129,413.61	159,863.87	1.24
CON-LEG101-OBA-1320	Granular Surround for Public Water Utility Distribution Piping [Outside E	13	17,762.27	17-Nov-26	01-Dec-26	13-May-26	18-May-26	0.00	17,762.27	0.00
CON-LEG101-OBA-1330	Installation of Micron Marker Magnetic Tape [Outside Boundary Area]	3	17,762.27	02-Dec-26	05-Dec-26	19-May-26	20-May-26	0.00	17,762.27	0.00
CON-LEG101-OBA-1340	Backfilling to Subgrade Elevation [Outside Boundary Area] 901 - 1800 r	10	35,526.47	06-Dec-26	16-Dec-26	21-May-26	23-May-26	0.00	35,526.47	0.00
CON-LEG101-OBA-1310	Testing for Public Water Utility Distribution Piping [Outside Boundary Ar	13	35,526.47	02-Nov-26	16-Nov-26	25-Jul-26	06-Sep-26	0.00	35,526.47	0.00
Valves/Chamber		29	120,600.00	02-Nov-26	23-Dec-26	03-Jun-26		0.00	118,188.00	0.00
CON-LEG101-OBA-1450	Installation of Air Valves [Outside Boundary Area] 901 - 1800 m	10	40,200.00	26-Nov-26	07-Dec-26	01-Aug-26		0.00	39,396.00	0.00
CON-LEG101-OBA-1440	Installation of Air Valve chambers [Outside Boundary Area] 901 - 1800	21	50,250.00	02-Nov-26	25-Nov-26	03-Jun-26		0.00	49,245.00	0.00
CON-LEG101-OBA-1510	Installation of Butterfly valves, on pipe with diameter 400 mm	6	30,150.00	17-Dec-26	23-Dec-26	03-Aug-26		0.00	29,547.00	0.00

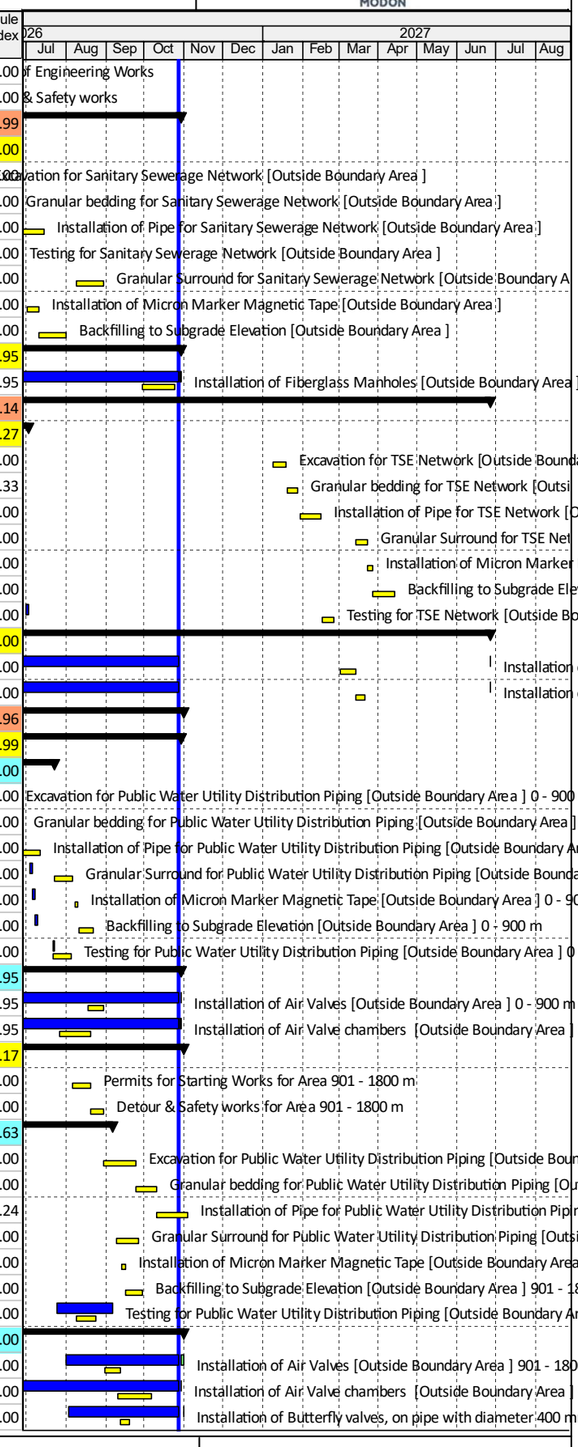


© Oracle Corporation

Activity ID	Activity Name	Original Duration	Budgeted Total Cost	BL Project Start	BL Project Finish	Actual Start	Actual Finish	Planned Value Cost	Earned Value Cost	Schedule Performance Index
Public Water Utility Distribution (1801 - 2780) m		79	355,252.27	24-Dec-26	04-May-27	25-Apr-26	07-Sep-26	0.00	355,252.27	0.00
CON-LEG101-OBA-1490	Permits for Starting Works for Area 1800 - 2780 m	12	0.00	24-Dec-26	06-Jan-27	25-Apr-26	25-Apr-26	0.00	0.00	0.00
CON-LEG101-OBA-1480	Detour & Safety works for Area 1800 - 2780 m	8	0.00	07-Jan-27	16-Jan-27	26-Apr-26	27-Apr-26	0.00	0.00	0.00
Pipe Work		73	355,252.27	17-Jan-27	04-May-27	28-Apr-26	07-Sep-26	0.00	355,252.27	0.00
CON-LEG101-OBA-1350	Excavation for Public Water Utility Distribution Piping [Outside Boundar	15	71,048.67	17-Jan-27	02-Feb-27	28-Apr-26	01-Sep-26	0.00	71,048.67	0.00
CON-LEG101-OBA-1360	Granular bedding for Public Water Utility Distribution Piping [Outside B	13	17,762.27	03-Feb-27	23-Feb-27	27-Jun-26	01-Sep-26	0.00	17,762.27	0.00
CON-LEG101-OBA-1370	Installation of Pipe for Public Water Utility Distribution Piping [Outside	21	159,863.87	24-Feb-27	20-Mar-27	30-Jun-26	02-Sep-26	0.00	159,863.87	0.00
CON-LEG101-OBA-1390	Granular Surround for Public Water Utility Distribution Piping [Outside E	13	17,762.27	05-Apr-27	19-Apr-27	02-Jul-26	02-Sep-26	0.00	17,762.27	0.00
CON-LEG101-OBA-1400	Installation of Micron Marker Magnetic Tape [Outside Boundary Area]	3	17,762.27	20-Apr-27	22-Apr-27	04-Jul-26	03-Sep-26	0.00	17,762.27	0.00
CON-LEG101-OBA-1410	Backfilling to Subgrade Elevation [Outside Boundary Area] 1800 - 2780	10	35,526.47	24-Apr-27	04-May-27	05-Jul-26	03-Sep-26	0.00	35,526.47	0.00
CON-LEG101-OBA-1380	Testing for Public Water Utility Distribution Piping [Outside Boundary Ar	13	35,526.47	21-Mar-27	04-Apr-27	07-Sep-26	07-Sep-26	0.00	35,526.47	0.00
Roads Finishing		210	8,138,565.00	25-Jan-27	03-Aug-27	06-May-26		0.00	6,317,961.34	0.00
Local – 01		163	3,747,145.05	20-Feb-27	20-Jul-27	06-May-26		0.00	3,148,408.40	0.00
LOCAL - 01 Segment-01 (From 0+000 to 1+066)		125	1,244,135.25	20-Feb-27	30-May-27	06-May-26		0.00	975,303.80	0.00
Concrete Curb		18	340,102.30	20-Feb-27	13-Mar-27	06-May-26	22-Oct-26	0.00	340,102.30	0.00
CON-LEG101-LR-6180	Installation of Precast Concrete Curb [Local – 01 Segment-01]	18	340,102.30	20-Feb-27	13-Mar-27	06-May-26	22-Oct-26	0.00	340,102.30	0.00
Asphalt Wearing Course		12	356,976.00	14-Mar-27	27-Mar-27	29-Sep-26		0.00	160,639.20	0.00
CON-LEG101-LR-5980	Tack coat (RC2) [Local – 01 Segment-01]	6	107,094.00	14-Mar-27	20-Mar-27	29-Sep-26		0.00	48,192.30	0.00
CON-LEG101-LR-6080	Bituminous wearing course [Local – 01 Segment-01]	6	249,882.00	21-Mar-27	27-Mar-27	29-Sep-26		0.00	112,446.90	0.00
Interlocking block roads/on-street parking		19	155,051.20	28-Mar-27	18-Apr-27	13-Jun-26	12-Oct-26	0.00	155,051.20	0.00
CON-LEG101-LR-6380	Interlocking block pavers for roads/on-street parking [Local – 01 Segr	19	155,051.20	28-Mar-27	18-Apr-27	13-Jun-26	12-Oct-26	0.00	155,051.20	0.00
Interlocking block sidewalk/footpath		19	271,691.70	19-Apr-27	10-May-27	26-Jun-26	26-Oct-26	0.00	271,691.70	0.00
CON-LEG101-LR-6280	Interlocking block pavers for sidewalk/footpath [Local – 01 Segment	19	271,691.70	19-Apr-27	10-May-27	26-Jun-26	26-Oct-26	0.00	271,691.70	0.00
Pavement Markings		16	34,585.05	05-Apr-27	22-Apr-27			0.00	0.00	0.00
CON-LEG101-LR-6580	Pavement Markings (White Paint/Yellow Paint) [Local – 01 Segment-	6	17,095.05	05-Apr-27	11-Apr-27			0.00	0.00	0.00
CON-LEG101-LR-6680	Handicap ramp [Local – 01 Segment-01]	10	17,490.00	12-Apr-27	22-Apr-27			0.00	0.00	0.00
Traffic Signs		58	85,729.00	24-Apr-27	30-May-27	05-Jul-26		0.00	47,819.40	0.00
CON-LEG101-LR-6480	Retroreflective Plastic Cones [Local – 01 Segment-01]	9	6,030.00	24-Apr-27	03-May-27			0.00	0.00	0.00
CON-LEG101-LR-6780	Installation of Traffic Signs [Local – 01 Segment-01]	19	79,699.00	04-May-27	30-May-27	05-Jul-26		0.00	47,819.40	0.00
LOCAL - 01 Segment-02 (From 1+066 to 2+133)		122	1,238,104.55	14-Mar-27	23-Jun-27	12-May-26		0.00	1,076,501.95	0.00
Concrete Curb		20	340,102.30	14-Mar-27	05-Apr-27	12-May-26	21-Jun-26	0.00	340,102.30	0.00
CON-LEG101-LR-6190	Installation of Precast Concrete Curb [Local – 01 Segment-02]	20	340,102.30	14-Mar-27	05-Apr-27	12-May-26	21-Jun-26	0.00	340,102.30	0.00
Asphalt Wearing Course		12	356,976.00	06-Apr-27	19-Apr-27	29-Sep-26		0.00	249,883.20	0.00
CON-LEG101-LR-5990	Tack coat (RC2) [Local – 01 Segment-02]	6	107,094.00	06-Apr-27	12-Apr-27	29-Sep-26		0.00	74,965.80	0.00
CON-LEG101-LR-6090	Bituminous wearing course [Local – 01 Segment-02]	6	249,882.00	13-Apr-27	19-Apr-27	29-Sep-26		0.00	174,917.40	0.00
Interlocking block roads/on-street parking		10	155,051.20	11-May-27	26-May-27	01-Jul-26	20-Jul-26	0.00	155,051.20	0.00
CON-LEG101-LR-6390	Interlocking block pavers for roads/on-street parking [Local – 01 Segr	10	155,051.20	11-May-27	26-May-27	01-Jul-26	20-Jul-26	0.00	155,051.20	0.00
Interlocking block sidewalk/footpath		10	271,691.00	27-May-27	07-Jun-27	01-Jul-26	20-Jul-26	0.00	271,691.00	0.00
CON-LEG101-LR-6290	Interlocking block pavers for sidewalk/footpath [Local – 01 Segment	10	271,691.00	27-May-27	07-Jun-27	01-Jul-26	20-Jul-26	0.00	271,691.00	0.00
Pavement Markings		25	34,585.05	12-Apr-27	10-May-27			0.00	0.00	0.00
CON-LEG101-LR-6590	Pavement Markings (White Paint/Yellow Paint) [Local – 01 Segment-	15	17,095.05	12-Apr-27	28-Apr-27			0.00	0.00	0.00
CON-LEG101-LR-6690	Handicap ramp [Local – 01 Segment-02]	10	17,490.00	29-Apr-27	10-May-27			0.00	0.00	0.00
Traffic Signs		57	79,699.00	11-May-27	23-Jun-27	06-Jul-26		0.00	59,774.25	0.00
CON-LEG101-LR-6490	Retroreflective Plastic Cones [Local – 01 Segment-02]	12	0.00	11-May-27	29-May-27			0.00	0.00	0.00
CON-LEG101-LR-6790	Installation of Traffic Signs [Local – 01 Segment-02]	21	79,699.00	31-May-27	23-Jun-27	06-Jul-26		0.00	59,774.25	0.00
LOCAL - 01 Segment-03 (From 2+133 to 3+200)		138	1,264,905.25	06-Apr-27	20-Jul-27	11-Jul-26		0.00	1,096,602.65	0.00
Concrete Curb		21	340,102.30	06-Apr-27	29-Apr-27	21-Jul-26	16-Sep-26	0.00	340,102.30	0.00
CON-LEG101-LR-6200	Installation of Precast Concrete Curb [Local – 01 Segment-03]	21	340,102.30	06-Apr-27	29-Apr-27	21-Jul-26	16-Sep-26	0.00	340,102.30	0.00
Asphalt Wearing Course		8	356,976.00	01-May-27	09-May-27	24-Oct-26		0.00	249,883.20	0.00
CON-LEG101-LR-6000	Tack coat (RC2) [Local – 01 Segment-03]	4	107,094.00	01-May-27	04-May-27	24-Oct-26		0.00	74,965.80	0.00
CON-LEG101-LR-6100	Bituminous wearing course [Local – 01 Segment-03]	4	249,882.00	05-May-27	09-May-27	24-Oct-26		0.00	174,917.40	0.00
Interlocking block roads/on-street parking		18	155,051.20	08-Jun-27	28-Jun-27	22-Aug-26	19-Sep-26	0.00	155,051.20	0.00
CON-LEG101-LR-6400	Interlocking block pavers for roads/on-street parking [Local – 01 Segr	18	155,051.20	08-Jun-27	28-Jun-27	22-Aug-26	19-Sep-26	0.00	155,051.20	0.00

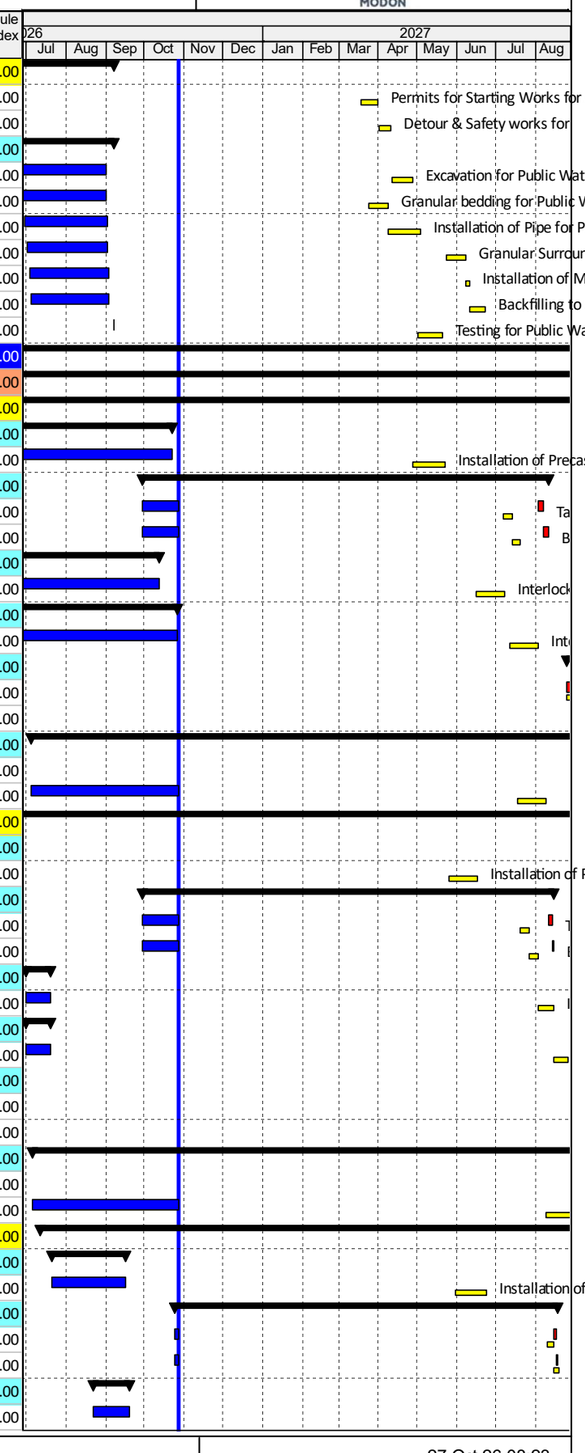


© Oracle Corporation

Activity ID	Activity Name	Original Duration	Budgeted Total Cost	BL Project Start	BL Project Finish	Actual Start	Actual Finish	Planned Value Cost	Earned Value Cost	Schedule Performance Index
Interlocking block sidewalk/footpath		19	271,691.70	29-Jun-27	20-Jul-27	22-Aug-26	20-Sep-26	0.00	271,691.70	0.00
CON-LEG101-LR-6300	Interlocking block pavers for sidewalk/footpath [Local – 01 Segment	19	271,691.70	29-Jun-27	20-Jul-27	22-Aug-26	20-Sep-26	0.00	271,691.70	0.00
Pavement Markings		22	34,585.05	01-May-27	30-May-27			0.00	0.00	0.00
CON-LEG101-LR-6600	Pavement Markings (White Paint/Yellow Paint) [Local – 01 Segment-	10	17,095.05	01-May-27	11-May-27			0.00	0.00	0.00
CON-LEG101-LR-6700	Handicap ramp [Local – 01 Segment-03]	12	17,490.00	12-May-27	30-May-27			0.00	0.00	0.00
Traffic Signs		50	106,499.00	31-May-27	18-Jul-27	11-Jul-26		0.00	79,874.25	0.00
CON-LEG101-LR-6500	Retroreflective Plastic Cones [Local – 01 Segment-03]	20	0.00	31-May-27	22-Jun-27			0.00	0.00	0.00
CON-LEG101-LR-6800	Installation of Traffic Signs [Local – 01 Segment-03]	21	106,499.00	24-Jun-27	18-Jul-27	11-Jul-26		0.00	79,874.25	0.00
Local – 02		176	643,592.80	25-Jan-27	14-Jul-27	09-Jun-26		0.00	590,568.45	0.00
Concrete Curb		15	158,713.70	25-Jan-27	15-Feb-27	09-Jun-26	24-Jun-26	0.00	158,713.70	0.00
CON-LEG101-LR-6210	Installation of Precast Concrete Curb [Local – 02]	15	158,713.70	25-Jan-27	15-Feb-27	09-Jun-26	24-Jun-26	0.00	158,713.70	0.00
Asphalt Wearing Course		5	237,984.00	10-May-27	19-May-27	04-Oct-26		0.00	214,185.60	0.00
CON-LEG101-LR-6010	Tack coat (RC2) [Local – 02]	2	71,394.00	10-May-27	11-May-27	04-Oct-26		0.00	64,254.60	0.00
CON-LEG101-LR-6110	Bituminous wearing course [Local – 02]	3	166,590.00	12-May-27	19-May-27	04-Oct-26		0.00	149,931.00	0.00
Interlocking block roads/on-street parking		21	72,356.80	20-May-27	13-Jun-27	18-Jul-26	28-Jul-26	0.00	72,356.80	0.00
CON-LEG101-LR-6410	Interlocking block pavers for roads/on-street parking [Local – 02]	21	72,356.80	20-May-27	13-Jun-27	18-Jul-26	28-Jul-26	0.00	72,356.80	0.00
Interlocking block sidewalk/footpath		21	126,789.60	14-Jun-27	07-Jul-27	18-Jul-26	28-Jul-26	0.00	126,789.60	0.00
CON-LEG101-LR-6310	Interlocking block pavers for sidewalk/footpath [Local – 02]	21	126,789.60	14-Jun-27	07-Jul-27	18-Jul-26	28-Jul-26	0.00	126,789.60	0.00
Pavement Markings		20	23,051.70	12-May-27	08-Jun-27			0.00	0.00	0.00
CON-LEG101-LR-6610	Pavement Markings (White Paint/Yellow Paint) [Local – 02]	10	11,396.70	12-May-27	27-May-27			0.00	0.00	0.00
CON-LEG101-LR-6710	Handicap ramp [Local – 02]	10	11,655.00	29-May-27	08-Jun-27			0.00	0.00	0.00
Traffic Signs		58	24,697.00	09-Jun-27	14-Jul-27	07-Jul-26		0.00	18,522.75	0.00
CON-LEG101-LR-6510	Retroreflective Plastic Cones [Local – 02]	10	0.00	09-Jun-27	20-Jun-27			0.00	0.00	0.00
CON-LEG101-LR-6810	Installation of Traffic Signs [Local – 02]	21	24,697.00	21-Jun-27	14-Jul-27	07-Jul-26		0.00	18,522.75	0.00
Local – 03		79	729,235.60	16-Feb-27	22-Jul-27	08-Jul-26		0.00	325,538.09	0.00
Concrete Curb		21	226,734.20	16-Feb-27	13-Mar-27	04-Oct-26		0.00	170,050.65	0.00
CON-LEG101-LR-6220	Installation of Precast Concrete Curb [Local – 03]	21	226,734.20	16-Feb-27	13-Mar-27	04-Oct-26		0.00	170,050.65	0.00
Asphalt Wearing Course		5	166,584.00	20-May-27	25-May-27			0.00	0.00	0.00
CON-LEG101-LR-6020	Tack coat (RC2) [Local – 03]	2	49,974.00	20-May-27	22-May-27			0.00	0.00	0.00
CON-LEG101-LR-6120	Bituminous wearing course [Local – 03]	3	116,610.00	23-May-27	25-May-27			0.00	0.00	0.00
Interlocking block roads/on-street parking		21	103,368.00	26-May-27	19-Jun-27			0.00	0.00	0.00
CON-LEG101-LR-6420	Interlocking block pavers for roads/on-street parking [Local – 03]	21	103,368.00	26-May-27	19-Jun-27			0.00	0.00	0.00
Interlocking block sidewalk/footpath		21	181,127.80	20-Jun-27	13-Jul-27	19-Oct-26		0.00	144,902.24	0.00
CON-LEG101-LR-6320	Interlocking block pavers for sidewalk/footpath [Local – 03]	21	181,127.80	20-Jun-27	13-Jul-27	19-Oct-26		0.00	144,902.24	0.00
Pavement Markings		20	16,137.60	26-May-27	17-Jun-27			0.00	0.00	0.00
CON-LEG101-LR-6620	Pavement Markings (White Paint/Yellow Paint) [Local – 03]	10	7,977.60	26-May-27	06-Jun-27			0.00	0.00	0.00
CON-LEG101-LR-6720	Handicap ramp [Local – 03]	10	8,160.00	07-Jun-27	17-Jun-27			0.00	0.00	0.00
Traffic Signs		35	35,284.00	19-Jun-27	22-Jul-27	08-Jul-26		0.00	10,585.20	0.00
CON-LEG101-LR-6520	Retroreflective Plastic Cones [Local – 03]	10	0.00	19-Jun-27	29-Jun-27			0.00	0.00	0.00
CON-LEG101-LR-6820	Installation of Traffic Signs [Local – 03]	20	35,284.00	30-Jun-27	22-Jul-27	08-Jul-26		0.00	10,585.20	0.00
Local – 04		70	565,205.55	14-Mar-27	21-Jul-27			0.00	0.00	0.00
Concrete Curb		21	158,714.75	14-Mar-27	06-Apr-27			0.00	0.00	0.00
CON-LEG101-LR-6230	Installation of Precast Concrete Curb [Local – 04]	21	158,714.75	14-Mar-27	06-Apr-27			0.00	0.00	0.00
Asphalt Wearing Course		5	166,584.00	26-May-27	31-May-27			0.00	0.00	0.00
CON-LEG101-LR-6030	Tack coat (RC2) [Local – 04]	2	49,974.00	26-May-27	27-May-27			0.00	0.00	0.00
CON-LEG101-LR-6130	Bituminous wearing course [Local – 04]	3	116,610.00	29-May-27	31-May-27			0.00	0.00	0.00
Interlocking block roads/on-street parking		19	72,357.60	01-Jun-27	22-Jun-27			0.00	0.00	0.00
CON-LEG101-LR-6430	Interlocking block pavers for roads/on-street parking [Local – 04]	19	72,357.60	01-Jun-27	22-Jun-27			0.00	0.00	0.00
Interlocking block sidewalk/footpath		19	126,789.60	23-Jun-27	14-Jul-27			0.00	0.00	0.00
CON-LEG101-LR-6330	Interlocking block pavers for sidewalk/footpath [Local – 04]	19	126,789.60	23-Jun-27	14-Jul-27			0.00	0.00	0.00
Pavement Markings		20	16,137.60	01-Jun-27	23-Jun-27			0.00	0.00	0.00
CON-LEG101-LR-6630	Pavement Markings (White Paint/Yellow Paint) [Local – 04]	10	7,977.60	01-Jun-27	12-Jun-27			0.00	0.00	0.00
CON-LEG101-LR-6730	Handicap ramp [Local – 04]	10	8,160.00	13-Jun-27	23-Jun-27			0.00	0.00	0.00

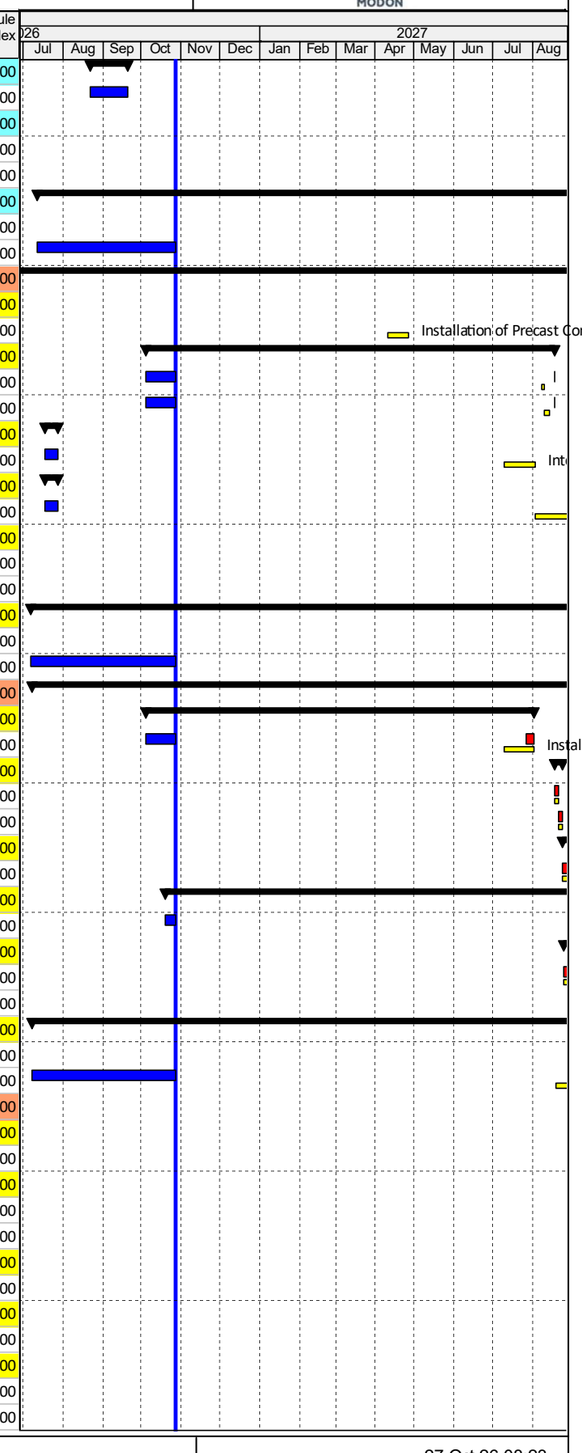


© Oracle Corporation

Activity ID	Activity Name	Original Duration	Budgeted Total Cost	BL Project Start	BL Project Finish	Actual Start	Actual Finish	Planned Value Cost	Earned Value Cost	Schedule Performance Index
Traffic Signs		24	24,622.00	24-Jun-27	21-Jul-27			0.00	0.00	0.00
CON-LEG101-LR-6530	Retroreflective Plastic Cones [Local – 04]	10	0.00	24-Jun-27	05-Jul-27			0.00	0.00	0.00
CON-LEG101-LR-6830	Installation of Traffic Signs [Local – 04]	14	24,622.00	06-Jul-27	21-Jul-27			0.00	0.00	0.00
Local – 05		133	939,406.25	07-Apr-27	19-Jul-27	24-May-26		0.00	865,080.90	0.00
Concrete Curb		16	272,081.85	07-Apr-27	25-Apr-27	24-May-26	28-Jun-26	0.00	272,081.85	0.00
CON-LEG101-LR-6240	Installation of Precast Concrete Curb [Local – 05]	16	272,081.85	07-Apr-27	25-Apr-27	24-May-26	28-Jun-26	0.00	272,081.85	0.00
Asphalt Wearing Course		5	261,780.00	01-Jun-27	06-Jun-27	03-Oct-26		0.00	222,513.00	0.00
CON-LEG101-LR-6040	Tack coat (RC2) [Local – 05]	2	78,534.00	01-Jun-27	02-Jun-27	03-Oct-26		0.00	66,753.90	0.00
CON-LEG101-LR-6140	Bituminous wearing course [Local – 05]	3	183,246.00	03-Jun-27	06-Jun-27	03-Oct-26		0.00	155,759.10	0.00
Interlocking block roads/on-street parking		18	124,040.80	07-Jun-27	27-Jun-27	13-Jul-26	29-Jul-26	0.00	124,040.80	0.00
CON-LEG101-LR-6440	Interlocking block pavers for roads/on-street parking [Local – 05]	18	124,040.80	07-Jun-27	27-Jun-27	13-Jul-26	29-Jul-26	0.00	124,040.80	0.00
Interlocking block sidewalk/footpath		19	217,353.50	28-Jun-27	19-Jul-27	13-Jul-26	29-Jul-26	0.00	217,353.50	0.00
CON-LEG101-LR-6340	Interlocking block pavers for sidewalk/footpath [Local – 05]	19	217,353.50	28-Jun-27	19-Jul-27	13-Jul-26	29-Jul-26	0.00	217,353.50	0.00
Pavement Markings		20	25,361.10	07-Jun-27	29-Jun-27			0.00	0.00	0.00
CON-LEG101-LR-6640	Pavement Markings (White Paint/Yellow Paint) [Local – 05]	10	12,536.10	07-Jun-27	17-Jun-27			0.00	0.00	0.00
CON-LEG101-LR-6740	Handicap ramp [Local – 05]	10	12,825.00	19-Jun-27	29-Jun-27			0.00	0.00	0.00
Traffic Signs		77	38,789.00	30-Jun-27	18-Jul-27	09-Jul-26		0.00	29,091.75	0.00
CON-LEG101-LR-6540	Retroreflective Plastic Cones [Local – 05]	5	0.00	30-Jun-27	05-Jul-27			0.00	0.00	0.00
CON-LEG101-LR-6840	Installation of Traffic Signs [Local – 05]	11	38,789.00	06-Jul-27	18-Jul-27	09-Jul-26		0.00	29,091.75	0.00
Local – 06		124	646,037.50	26-Apr-27	27-Jul-27	10-Jun-26		0.00	563,419.25	0.00
Concrete Curb		21	181,387.55	26-Apr-27	24-May-27	10-Jun-26	15-Jul-26	0.00	181,387.55	0.00
CON-LEG101-LR-6250	Installation of Precast Concrete Curb [Local – 06]	21	181,387.55	26-Apr-27	24-May-27	10-Jun-26	15-Jul-26	0.00	181,387.55	0.00
Asphalt Wearing Course		5	190,386.00	07-Jun-27	12-Jun-27	06-Oct-26		0.00	133,270.20	0.00
CON-LEG101-LR-6050	Tack coat (RC2) [Local – 06]	3	57,114.00	07-Jun-27	09-Jun-27	06-Oct-26		0.00	39,979.80	0.00
CON-LEG101-LR-6150	Bituminous wearing course [Local – 06]	2	133,272.00	10-Jun-27	12-Jun-27	06-Oct-26		0.00	93,290.40	0.00
Interlocking block roads/on-street parking		19	82,694.40	13-Jun-27	04-Jul-27	19-Jul-26	20-Aug-26	0.00	82,694.40	0.00
CON-LEG101-LR-6450	Interlocking block pavers for roads/on-street parking [Local – 06]	19	82,694.40	13-Jun-27	04-Jul-27	19-Jul-26	20-Aug-26	0.00	82,694.40	0.00
Interlocking block sidewalk/footpath		19	144,902.10	05-Jul-27	26-Jul-27	19-Jul-26	20-Aug-26	0.00	144,902.10	0.00
CON-LEG101-LR-6350	Interlocking block pavers for sidewalk/footpath [Local – 06]	19	144,902.10	05-Jul-27	26-Jul-27	19-Jul-26	20-Aug-26	0.00	144,902.10	0.00
Pavement Markings		20	18,447.45	13-Jun-27	05-Jul-27			0.00	0.00	0.00
CON-LEG101-LR-6650	Pavement Markings (White Paint/Yellow Paint) [Local – 06]	10	9,117.45	13-Jun-27	23-Jun-27			0.00	0.00	0.00
CON-LEG101-LR-6750	Handicap ramp [Local – 06]	10	9,330.00	24-Jun-27	05-Jul-27			0.00	0.00	0.00
Traffic Signs		74	28,220.00	06-Jul-27	27-Jul-27	11-Jul-26		0.00	21,165.00	0.00
CON-LEG101-LR-6550	Retroreflective Plastic Cones [Local – 06]	4	0.00	06-Jul-27	10-Jul-27			0.00	0.00	0.00
CON-LEG101-LR-6850	Installation of Traffic Signs [Local – 06]	15	28,220.00	11-Jul-27	27-Jul-27	11-Jul-26		0.00	21,165.00	0.00
Local – 07		84	161,512.20	25-May-27	21-Jul-27	05-Jul-26		0.00	150,384.85	0.00
Concrete Curb		8	45,346.65	25-May-27	02-Jun-27	05-Jul-26	20-Jul-26	0.00	45,346.65	0.00
CON-LEG101-LR-6260	Installation of Precast Concrete Curb [Local – 07]	8	45,346.65	25-May-27	02-Jun-27	05-Jul-26	20-Jul-26	0.00	45,346.65	0.00
Asphalt Wearing Course		12	47,616.00	03-Jun-27	16-Jun-27	01-Oct-26		0.00	42,854.40	0.00
CON-LEG101-LR-6060	Tack coat (RC2) [Local – 07]	6	14,298.00	03-Jun-27	09-Jun-27	01-Oct-26		0.00	12,868.20	0.00
CON-LEG101-LR-6160	Bituminous wearing course [Local – 07]	6	33,318.00	10-Jun-27	16-Jun-27	01-Oct-26		0.00	29,986.20	0.00
Interlocking block roads/on-street parking		15	20,673.60	17-Jun-27	04-Jul-27	23-Jul-26	02-Aug-26	0.00	20,673.60	0.00
CON-LEG101-LR-6460	Interlocking block pavers for roads/on-street parking [Local – 07]	15	20,673.60	17-Jun-27	04-Jul-27	23-Jul-26	02-Aug-26	0.00	20,673.60	0.00
Interlocking block sidewalk/footpath		15	36,225.70	05-Jul-27	21-Jul-27	23-Jul-26	02-Aug-26	0.00	36,225.70	0.00
CON-LEG101-LR-6360	Interlocking block pavers for sidewalk/footpath [Local – 07]	15	36,225.70	05-Jul-27	21-Jul-27	23-Jul-26	02-Aug-26	0.00	36,225.70	0.00
Pavement Markings		8	4,604.25	17-Jun-27	26-Jun-27			0.00	0.00	0.00
CON-LEG101-LR-6660	Pavement Markings (White Paint/Yellow Paint) [Local – 07]	4	2,279.25	17-Jun-27	21-Jun-27			0.00	0.00	0.00
CON-LEG101-LR-6760	Handicap ramp [Local – 07]	4	2,325.00	22-Jun-27	26-Jun-27			0.00	0.00	0.00
Traffic Signs		72	7,046.00	27-Jun-27	17-Jul-27	12-Jul-26		0.00	5,284.50	0.00
CON-LEG101-LR-6560	Retroreflective Plastic Cones [Local – 07]	4	0.00	27-Jun-27	30-Jun-27			0.00	0.00	0.00
CON-LEG101-LR-6860	Installation of Traffic Signs [Local – 07]	14	7,046.00	01-Jul-27	17-Jul-27	12-Jul-26		0.00	5,284.50	0.00
Local – 08		95	706,430.05	03-Jun-27	03-Aug-27	13-Jul-26		0.00	674,561.40	0.00
Concrete Curb		14	204,061.40	03-Jun-27	19-Jun-27	23-Jul-26	03-Sep-26	0.00	204,061.40	0.00

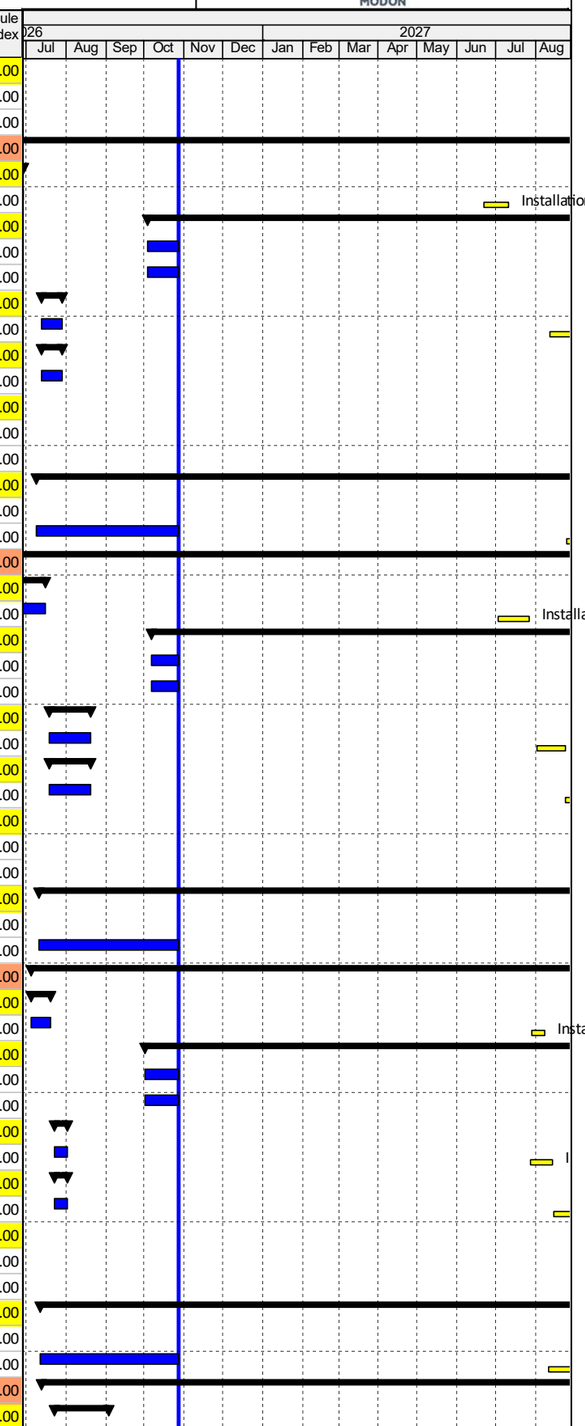


© Oracle Corporation

Activity ID	Activity Name	Original Duration	Budgeted Total Cost	BL Project Start	BL Project Finish	Actual Start	Actual Finish	Planned Value Cost	Earned Value Cost	Schedule Performance Index
CON-LEG101-LR-6270	Installation of Precast Concrete Curb [Local – 08]	14	204,061.40	03-Jun-27	19-Jun-27	23-Jul-26	03-Sep-26	0.00	204,061.40	0.00
Asphalt Wearing Course		5	188,004.00	20-Jun-27	24-Jun-27	24-Oct-26	24-Oct-26	0.00	188,004.00	0.00
CON-LEG101-LR-6070	Tack coat (RC2) [Local – 08]	2	71,394.00	20-Jun-27	21-Jun-27	24-Oct-26	24-Oct-26	0.00	71,394.00	0.00
CON-LEG101-LR-6170	Bituminous wearing course [Local – 08]	3	116,610.00	22-Jun-27	24-Jun-27	24-Oct-26	24-Oct-26	0.00	116,610.00	0.00
Interlocking block roads/on-street parking		13	93,031.20	26-Jun-27	10-Jul-27	12-Sep-26	16-Sep-26	0.00	93,031.20	0.00
CON-LEG101-LR-6470	Interlocking block pavers for roads/on-street parking [Local – 08]	13	93,031.20	26-Jun-27	10-Jul-27	12-Sep-26	16-Sep-26	0.00	93,031.20	0.00
Interlocking block sidewalk/footpath		21	163,015.30	11-Jul-27	03-Aug-27	13-Sep-26	17-Sep-26	0.00	163,015.30	0.00
CON-LEG101-LR-6370	Interlocking block pavers for sidewalk/footpath [Local – 08]	21	163,015.30	11-Jul-27	03-Aug-27	13-Sep-26	17-Sep-26	0.00	163,015.30	0.00
Pavement Markings		8	23,052.15	26-Jun-27	04-Jul-27			0.00	0.00	0.00
CON-LEG101-LR-6670	Pavement Markings (White Paint/Yellow Paint) [Local – 08]	4	11,397.15	26-Jun-27	29-Jun-27			0.00	0.00	0.00
CON-LEG101-LR-6770	Handicap ramp [Local – 08]	4	11,655.00	30-Jun-27	04-Jul-27			0.00	0.00	0.00
Traffic Signs		63	35,266.00	05-Jul-27	25-Jul-27	13-Jul-26		0.00	26,449.50	0.00
CON-LEG101-LR-6570	Retroreflective Plastic Cones [Local – 08]	4	0.00	05-Jul-27	08-Jul-27			0.00	0.00	0.00
CON-LEG101-LR-6870	Installation of Traffic Signs [Local – 08]	14	35,266.00	10-Jul-27	25-Jul-27	13-Jul-26		0.00	26,449.50	0.00
Fence and Gate		563	8,127,691.90	07-Feb-26	18-Oct-27	10-Dec-25		2,216,939.10	5,352,415.58	2.41
Fence and Gate Segment -01 (From 0+000 to 0+671)		326	1,109,838.30	07-Feb-26	22-Jun-26	10-Dec-25		1,109,838.30	44,979.82	0.04
Fence		326	1,109,838.30	07-Feb-26	22-Jun-26	10-Dec-25		1,109,838.30	44,979.82	0.04
CON-LEG101-FG-1000	Excavation for Fences [Fence and Gate Segment -01]	10	3,941.20	07-Feb-26	17-Feb-26	10-Dec-25		3,941.20	3,350.02	0.85
CON-LEG101-FG-1050	Concrete Works for Ground Beam for Fences [Fence and Gate Segme	20	200,048.00	14-Apr-26	06-May-26			200,048.00	0.00	0.00
CON-LEG101-FG-1260	Embankments to the Fences [Fence and Gate Segment -01]	8	41,176.80	05-Apr-26	13-Apr-26			41,176.80	0.00	0.00
CON-LEG101-FG-1420	Plster Works for Fences [Fence and Gate Segment -01]	12	16,329.00	07-May-26	20-May-26			16,329.00	0.00	0.00
CON-LEG101-FG-1100	Lean concrete for Foundation [Fence and Gate Segment -01]	4	18,814.00	18-Feb-26	23-Feb-26	21-Dec-25		18,814.00	3,762.80	0.20
CON-LEG101-FG-1150	Reinforced concrete Structure [Fence and Gate Segment -01]	20	189,335.00	24-Feb-26	18-Mar-26	23-Dec-25		189,335.00	37,867.00	0.20
CON-LEG101-FG-1200	Spraying of bituminous paint waterproofing for R.C foundation [Fence a	10	39,255.30	19-Mar-26	04-Apr-26			39,255.30	0.00	0.00
CON-LEG101-FG-1280	Installation of Metal Fence [Fence and Gate Segment -01]	14	584,610.00	21-May-26	10-Jun-26			584,610.00	0.00	0.00
CON-LEG101-FG-1340	Paint On Cement Plaster [Fence and Gate Segment -01]	10	16,329.00	11-Jun-26	22-Jun-26			16,329.00	0.00	0.00
Fence and Gate Segment -02 (From 0+671 to 1+342)		215	1,109,822.30	23-Jun-26	29-Oct-26	25-Mar-26		1,107,100.80	652,515.16	0.59
Fence		215	1,109,822.30	23-Jun-26	29-Oct-26	25-Mar-26		1,107,100.80	652,515.16	0.59
CON-LEG101-FG-1010	Excavation for Fences [Fence and Gate Segment -02]	10	3,941.20	23-Jun-26	04-Jul-26	25-Mar-26		3,941.20	3,350.02	0.85
CON-LEG101-FG-1060	Concrete Works for Ground Beam for Fences [Fence and Gate Segme	20	200,032.00	23-Aug-26	14-Sep-26	12-May-26		200,032.00	170,027.20	0.85
CON-LEG101-FG-1330	Embankments to the Fences [Fence and Gate Segment -02]	8	41,176.80	13-Aug-26	22-Aug-26	09-May-26		41,176.80	35,000.28	0.85
CON-LEG101-FG-1430	Plster Works for Fences [Fence and Gate Segment -02]	12	16,329.00	15-Sep-26	29-Sep-26			16,329.00	0.00	0.00
CON-LEG101-FG-1110	Lean concrete for Foundation [Fence and Gate Segment -02]	4	18,814.00	05-Jul-26	08-Jul-26	02-Apr-26		18,814.00	15,991.90	0.85
CON-LEG101-FG-1160	Reinforced concrete Structure [Fence and Gate Segment -02]	20	189,335.00	09-Jul-26	01-Aug-26	04-Apr-26		189,335.00	160,934.75	0.85
CON-LEG101-FG-1210	Spraying of bituminous paint waterproofing for R.C foundation [Fence a	10	39,255.30	02-Aug-26	12-Aug-26	02-May-26		39,255.30	33,367.01	0.85
CON-LEG101-FG-1290	Installation of Metal Fence [Fence and Gate Segment -02]	14	584,610.00	30-Sep-26	15-Oct-26	02-Sep-26		584,610.00	233,844.00	0.40
CON-LEG101-FG-1350	Paint On Cement Plaster [Fence and Gate Segment -02]	12	16,329.00	17-Oct-26	29-Oct-26			13,607.50	0.00	0.00
Fence and Gate Segment -03 (From 1+342 to 2+014)		188	3,688,384.30	31-Oct-26	14-Apr-27	25-Jan-26		0.00	3,546,731.20	0.00
Fence		136	3,583,864.30	31-Oct-26	13-Mar-27	25-Jan-26		0.00	3,546,731.20	0.00
CON-LEG101-FG-1020	Excavation for Fences [Fence and Gate Segment -03]	10	3,941.20	31-Oct-26	10-Nov-26	25-Jan-26	17-Mar-26	0.00	3,941.20	0.00
CON-LEG101-FG-1120	Lean concrete for Foundation [Fence and Gate Segment -03]	4	18,814.00	11-Nov-26	15-Nov-26	31-Jan-26	20-Apr-26	0.00	18,814.00	0.00
CON-LEG101-FG-1170	Reinforced concrete Structure [Fence and Gate Segment -03]	20	2,663,377.00	16-Nov-26	08-Dec-26	11-Feb-26	27-Jul-26	0.00	2,663,377.00	0.00
CON-LEG101-FG-1220	Spraying of bituminous paint waterproofing for R.C foundation [Fence a	10	39,255.30	09-Dec-26	20-Dec-26	18-Feb-26	04-Aug-26	0.00	39,255.30	0.00
CON-LEG101-FG-1390	Embankments to the Fences [Fence and Gate Segment -03]	8	41,176.80	21-Dec-26	29-Dec-26	01-Apr-26	09-Aug-26	0.00	41,176.80	0.00
CON-LEG101-FG-1070	Concrete Works for Ground Beam for Fences [Fence and Gate Segme	20	200,032.00	30-Dec-26	21-Jan-27	11-Apr-26	20-Aug-26	0.00	200,032.00	0.00
CON-LEG101-FG-1440	Plster Works for Fences [Fence and Gate Segment -03]	12	16,329.00	23-Jan-27	04-Feb-27	01-Aug-26		0.00	6,531.60	0.00
CON-LEG101-FG-1300	Installation of Metal Fence [Fence and Gate Segment -03]	14	584,610.00	06-Feb-27	27-Feb-27	14-May-26		0.00	567,071.70	0.00
CON-LEG101-FG-1360	Paint On Cement Plaster [Fence and Gate Segment -03]	12	16,329.00	28-Feb-27	13-Mar-27	19-Sep-26		0.00	6,531.60	0.00
Gate		40	104,520.00	28-Feb-27	14-Apr-27			0.00	0.00	0.00
CON-LEG101-FG-1250	Installation of Main Entrance Motorized Gate [Fence and Gate Segment	20	80,400.00	28-Feb-27	22-Mar-27			0.00	0.00	0.00
CON-LEG101-FG-1270	Installation of Pedestrain Gate [Fence and Gate Segment -03]	20	24,120.00	23-Mar-27	14-Apr-27			0.00	0.00	0.00
Fence and Gate Segment -04 (From 2+014 to 2+685)		124	1,109,822.30	14-Mar-27	13-Jul-27	25-Dec-25		0.00	1,108,189.40	0.00
Fence		124	1,109,822.30	14-Mar-27	13-Jul-27	25-Dec-25		0.00	1,108,189.40	0.00

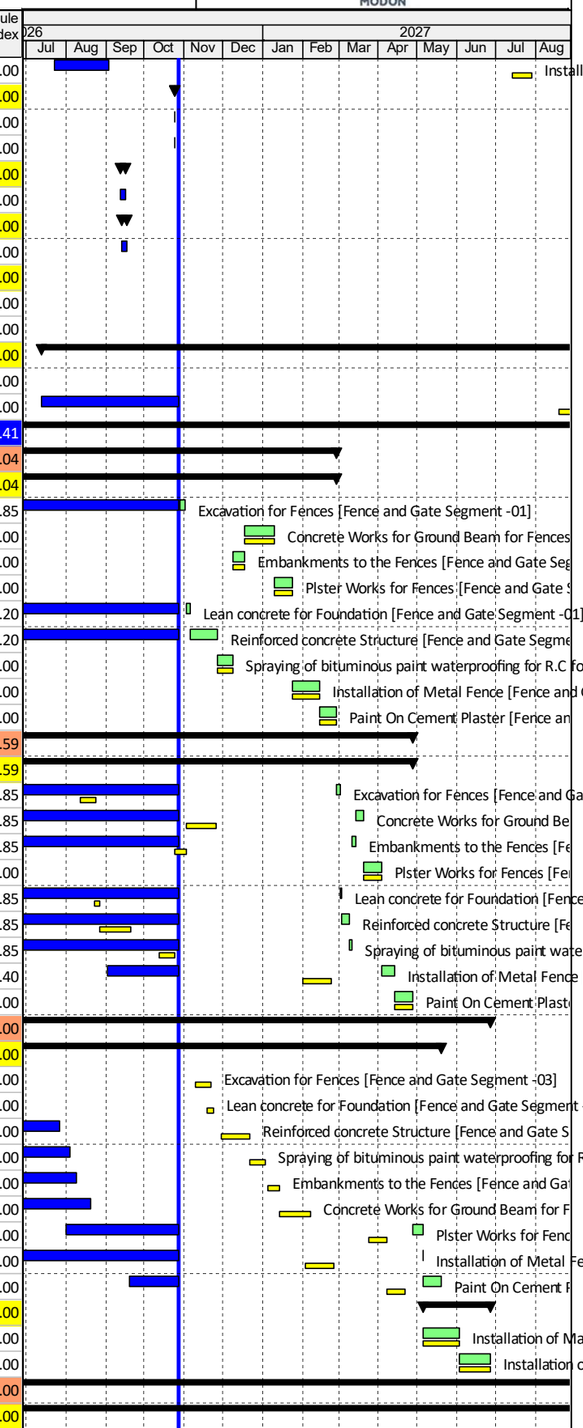


© Oracle Corporation

Activity ID	Activity Name	Original Duration	Budgeted Total Cost	BL Project Start	BL Project Finish	Actual Start	Actual Finish	Planned Value Cost	Earned Value Cost	Schedule Performance Index
CON-LEG101-FG-1030	Excavation for Fences [Fence and Gate Segment -04]	10	3,941.20	14-Mar-27	24-Mar-27	25-Dec-25	27-Jan-26	0.00	3,941.20	0.00
CON-LEG101-FG-1130	Lean concrete for Foundation [Fence and Gate Segment -04]	4	18,814.00	25-Mar-27	29-Mar-27	06-Jan-26	18-Feb-26	0.00	18,814.00	0.00
CON-LEG101-FG-1180	Reinforced concrete Structure [Fence and Gate Segment -04]	20	189,335.00	30-Mar-27	21-Apr-27	07-Jan-26	15-Apr-26	0.00	189,335.00	0.00
CON-LEG101-FG-1230	Spraying of bituminous paint waterproofing for R.C foundation [Fence a	10	39,255.30	22-Apr-27	03-May-27	13-Jan-26	16-Apr-26	0.00	39,255.30	0.00
CON-LEG101-FG-1400	Embankments to the Fences [Fence and Gate Segment -04]	8	41,176.80	04-May-27	12-May-27	10-Feb-26	22-Apr-26	0.00	41,176.80	0.00
CON-LEG101-FG-1080	Concrete Works for Ground Beam for Fences [Fence and Gate Segme	20	200,032.00	13-May-27	09-Jun-27	17-Jan-26	30-Jun-26	0.00	200,032.00	0.00
CON-LEG101-FG-1310	Installation of Metal Fence [Fence and Gate Segment -04]	7	584,610.00	22-Jun-27	29-Jun-27	22-Apr-26	19-Aug-26	0.00	584,610.00	0.00
CON-LEG101-FG-1450	Plster Works for Fences [Fence and Gate Segment -04]	10	16,329.00	10-Jun-27	21-Jun-27	01-Sep-26		0.00	15,512.55	0.00
CON-LEG101-FG-1370	Paint On Cement Plaster [Fence and Gate Segment -04]	12	16,329.00	30-Jun-27	13-Jul-27	11-May-26		0.00	15,512.55	0.00
Fence and Gate Segment -05 (From 2+685 to 3+356)		82	1,109,824.70	14-Jul-27	18-Oct-27			0.00	0.00	0.00
Fence		82	1,109,824.70	14-Jul-27	18-Oct-27			0.00	0.00	0.00
CON-LEG101-FG-1040	Excavation for Fences [Fence and Gate Segment -05]	10	3,941.20	14-Jul-27	25-Jul-27			0.00	0.00	0.00
CON-LEG101-FG-1090	Concrete Works for Ground Beam for Fences [Fence and Gate Segme	15	200,032.00	08-Sep-27	26-Sep-27			0.00	0.00	0.00
CON-LEG101-FG-1410	Embankments to the Fences [Fence and Gate Segment -05]	4	41,176.80	04-Sep-27	07-Sep-27			0.00	0.00	0.00
CON-LEG101-FG-1460	Plster Works for Fences [Fence and Gate Segment -05]	6	16,329.00	27-Sep-27	03-Oct-27			0.00	0.00	0.00
CON-LEG101-FG-1140	Lean concrete for Foundation [Fence and Gate Segment -05]	4	18,814.00	26-Jul-27	29-Jul-27			0.00	0.00	0.00
CON-LEG101-FG-1190	Reinforced concrete Structure [Fence and Gate Segment -05]	20	189,335.00	31-Jul-27	22-Aug-27			0.00	0.00	0.00
CON-LEG101-FG-1240	Spraying of bituminous paint waterproofing for R.C foundation [Fence a	10	39,255.30	23-Aug-27	02-Sep-27			0.00	0.00	0.00
CON-LEG101-FG-1320	Installation of Metal Fence [Fence and Gate Segment -05]	7	584,610.00	04-Oct-27	11-Oct-27			0.00	0.00	0.00
CON-LEG101-FG-1380	Paint On Cement Plaster [Fence and Gate Segment -05]	6	16,331.40	12-Oct-27	18-Oct-27			0.00	0.00	0.00
Roundabout & Landscape		227	2,047,352.90	14-Mar-27	18-Oct-27			0.00	0.00	0.00
Local – 01		168	705,970.70	14-Mar-27	10-Oct-27			0.00	0.00	0.00
LOCAL - 01 Segment-01 (From 0+000 to 1+066)		141	513,701.90	14-Mar-27	09-Oct-27			0.00	0.00	0.00
Irrigation Works		101	408,833.80	14-Mar-27	22-Jul-27			0.00	0.00	0.00
Secondary Irrigation		101	408,833.80	14-Mar-27	22-Jul-27			0.00	0.00	0.00
Pipe Work		60	124,402.80	14-Mar-27	05-Jun-27			0.00	0.00	0.00
CON-LEG101-LR-4870	Excavation for Secondary Irrigation [Local – 01 Segment-01]	8	1,241.40	14-Mar-27	22-Mar-27			0.00	0.00	0.00
CON-LEG101-LR-4940	Sand bedding for Secondary Irrigation [Local – 01 Segment-01]	5	0.00	23-Mar-27	28-Mar-27			0.00	0.00	0.00
CON-LEG101-LR-5010	Installation of Pipe for Secondary Irrigation [Local – 01 Segment-01]	10	3,715.20	29-Mar-27	08-Apr-27			0.00	0.00	0.00
CON-LEG101-LR-5080	Sand Surround for Secondary Irrigation [Local – 01 Segment-01]	5	0.00	10-Apr-27	14-Apr-27			0.00	0.00	0.00
CON-LEG101-LR-5150	Installation of Micron Marker Magnetic Tape [Local – 01 Segment-01]	10	0.00	15-Apr-27	26-Apr-27			0.00	0.00	0.00
CON-LEG101-LR-5210	Backfilling to Subgrade Elevation [Local – 01 Segment-01]	5	1,237.80	27-Apr-27	02-May-27			0.00	0.00	0.00
CON-LEG101-LR-5410	Installation of tubing for risers connections from laterals [Local – 01 Seg	17	118,208.40	12-May-27	05-Jun-27			0.00	0.00	0.00
Valves and Controller		41	284,431.00	06-Jun-27	22-Jul-27			0.00	0.00	0.00
CON-LEG101-LR-5270	Installation of Electrical Solenoid Valve [Local – 01 Segment-01]	5	4,355.00	06-Jun-27	10-Jun-27			0.00	0.00	0.00
CON-LEG101-LR-5310	Installation of quick coupler valve [Local – 01 Segment-01]	5	6,030.00	12-Jun-27	16-Jun-27			0.00	0.00	0.00
CON-LEG101-LR-5350	Installation of a Flush valve [Local – 01 Segment-01]	5	13,400.00	17-Jun-27	22-Jun-27			0.00	0.00	0.00
CON-LEG101-LR-5470	Installation of Advanced Irrigation controller [Local – 01 Segment-01]	7	234,500.00	23-Jun-27	30-Jun-27			0.00	0.00	0.00
CON-LEG101-LR-5480	Install single station decoder for valve connection [Local – 01 Segment-	7	6,700.00	01-Jul-27	08-Jul-27			0.00	0.00	0.00
CON-LEG101-LR-5520	Installation of Decoder cables 12 AWG between valves and controllers [	12	19,446.00	10-Jul-27	22-Jul-27			0.00	0.00	0.00
Curbs and edging		2	4,100.40	24-Jul-27	25-Jul-27			0.00	0.00	0.00
CON-LEG101-LR-4790	Installation of Curbs and edging [Local – 01 Segment-01]	2	4,100.40	24-Jul-27	25-Jul-27			0.00	0.00	0.00
Landscape		38	100,767.70	26-Jul-27	09-Oct-27			0.00	0.00	0.00
CON-LEG101-LR-4580	Site preparation for Planting Area [Local – 01 Segment-01]	9	20,153.10	26-Jul-27	04-Aug-27			0.00	0.00	0.00
CON-LEG101-LR-4650	Placing Agricutural Soil [Local – 01 Segment-01]	9	20,155.30	05-Aug-27	15-Aug-27			0.00	0.00	0.00
CON-LEG101-LR-4720	Planting Shrubs And Ground Cover [Local – 01 Segment-01]	20	60,459.30	15-Sep-27	09-Oct-27			0.00	0.00	0.00
LOCAL - 01 Segment-02 (From 1+066 to 2+133)		107	94,626.90	06-Jun-27	09-Oct-27			0.00	0.00	0.00
Irrigation Works		78	59,671.60	06-Jun-27	04-Sep-27			0.00	0.00	0.00
Secondary Irrigation		78	59,671.60	06-Jun-27	04-Sep-27			0.00	0.00	0.00
Pipe Work		47	41,464.20	06-Jun-27	29-Jul-27			0.00	0.00	0.00
CON-LEG101-LR-4880	Excavation for Secondary Irrigation [Local – 01 Segment-02]	5	412.00	06-Jun-27	10-Jun-27			0.00	0.00	0.00
CON-LEG101-LR-4950	Sand bedding for Secondary Irrigation [Local – 01 Segment-02]	5	0.00	12-Jun-27	16-Jun-27			0.00	0.00	0.00
CON-LEG101-LR-5020	Installation of Pipe for Secondary Irrigation [Local – 01 Segment-02]	5	1,237.80	17-Jun-27	22-Jun-27			0.00	0.00	0.00

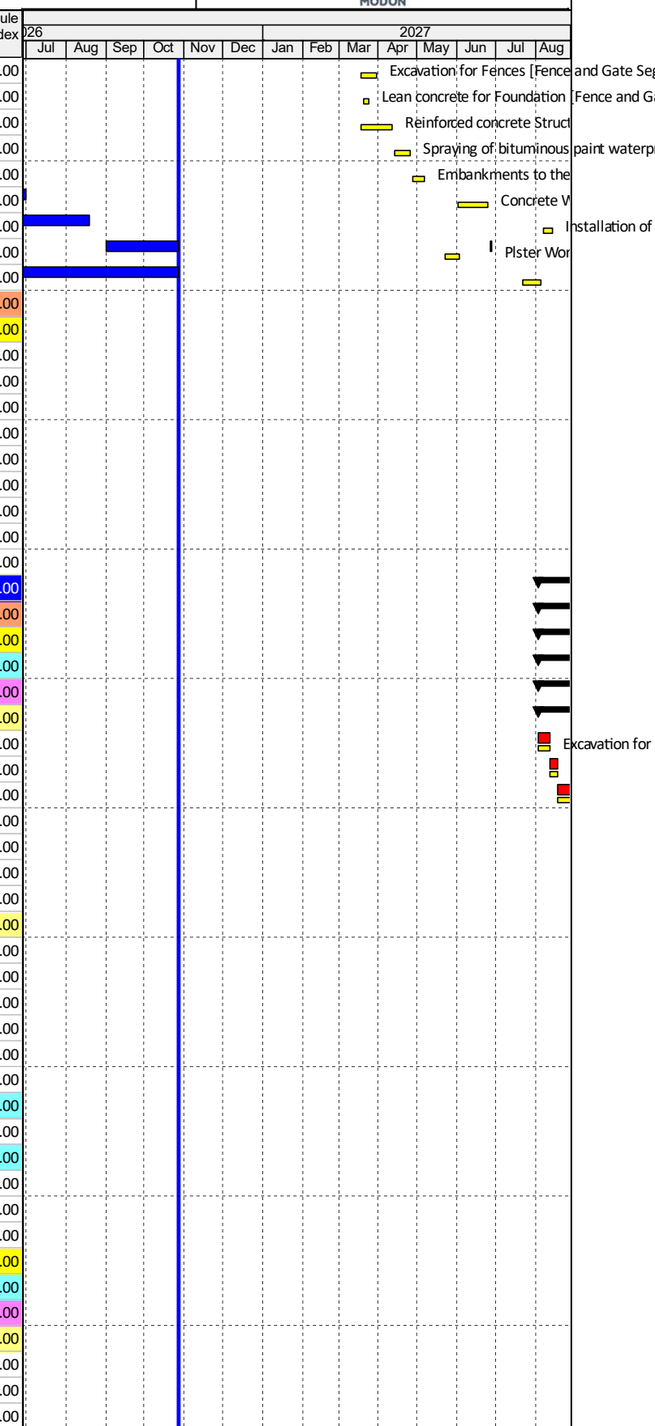


© Oracle Corporation

Activity ID	Activity Name	Original Duration	Budgeted Total Cost	BL Project Start	BL Project Finish	Actual Start	Actual Finish	Planned Value Cost	Earned Value Cost	Schedule Performance Index
CON-LEG101-LR-5090	Sand Surround for Secondary Irrigation [Local – 01 Segment-02]	5	0.00	23-Jun-27	28-Jun-27			0.00	0.00	0.00
CON-LEG101-LR-5160	Installation of Micron Marker Magnetic Tape [Local – 01 Segment-02]	5	0.00	29-Jun-27	04-Jul-27			0.00	0.00	0.00
CON-LEG101-LR-5220	Backfilling to Subgrade Elevation [Local – 01 Segment-02]	5	412.00	05-Jul-27	10-Jul-27			0.00	0.00	0.00
CON-LEG101-LR-5420	Installation of tubing for risers connections from laterals [Local – 01 Seg	17	39,402.40	11-Jul-27	29-Jul-27			0.00	0.00	0.00
Valves and Controller		17	18,207.40	16-Aug-27	04-Sep-27			0.00	0.00	0.00
CON-LEG101-LR-5360	Installation of a Flush valve [Local – 01 Segment-02]	5	11,725.00	16-Aug-27	21-Aug-27			0.00	0.00	0.00
CON-LEG101-LR-5530	Installation of Decoder cables 12 AWG between valves and controllers [	12	6,482.40	22-Aug-27	04-Sep-27			0.00	0.00	0.00
Curbs and edging		2	1,366.80	05-Sep-27	06-Sep-27			0.00	0.00	0.00
CON-LEG101-LR-4800	Installation of Curbs and edging [Local – 01 Segment-02]	2	1,366.80	05-Sep-27	06-Sep-27			0.00	0.00	0.00
Landscape		27	33,588.50	07-Sep-27	09-Oct-27			0.00	0.00	0.00
CON-LEG101-LR-4590	Site preparation for Planting Area [Local – 01 Segment-02]	9	6,717.70	07-Sep-27	16-Sep-27			0.00	0.00	0.00
CON-LEG101-LR-4660	Placing Agricutural Soil [Local – 01 Segment-02]	9	6,717.70	18-Sep-27	28-Sep-27			0.00	0.00	0.00
CON-LEG101-LR-4730	Planting Shrubs And Ground Cover [Local – 01 Segment-02]	9	20,153.10	29-Sep-27	09-Oct-27			0.00	0.00	0.00
LOCAL - 01 Segment-03 (From 2+133 to 3+200)		61	97,641.90	31-Jul-27	10-Oct-27			0.00	0.00	0.00
Irrigation Works		56	62,686.60	31-Jul-27	04-Oct-27			0.00	0.00	0.00
Secondary Irrigation		56	62,686.60	31-Jul-27	04-Oct-27			0.00	0.00	0.00
Pipe Work		56	41,464.20	31-Jul-27	04-Oct-27			0.00	0.00	0.00
CON-LEG101-LR-4890	Excavation for Secondary Irrigation [Local – 01 Segment-03]	5	412.00	31-Jul-27	04-Aug-27			0.00	0.00	0.00
CON-LEG101-LR-4960	Sand bedding for Secondary Irrigation [Local – 01 Segment-03]	5	0.00	05-Aug-27	10-Aug-27			0.00	0.00	0.00
CON-LEG101-LR-5030	Installation of Pipe for Secondary Irrigation [Local – 01 Segment-03]	5	1,237.80	11-Aug-27	16-Aug-27			0.00	0.00	0.00
CON-LEG101-LR-5100	Sand Surround for Secondary Irrigation [Local – 01 Segment-03]	8	0.00	17-Aug-27	25-Aug-27			0.00	0.00	0.00
CON-LEG101-LR-5170	Installation of Micron Marker Magnetic Tape [Local – 01 Segment-03]	8	0.00	26-Aug-27	04-Sep-27			0.00	0.00	0.00
CON-LEG101-LR-5230	Backfilling to Subgrade Elevation [Local – 01 Segment-03]	8	412.00	05-Sep-27	13-Sep-27			0.00	0.00	0.00
CON-LEG101-LR-5430	Installation of tubing for risers connections from laterals [Local – 01 Seg	17	39,402.40	14-Sep-27	04-Oct-27			0.00	0.00	0.00
Valves and Controller		17	21,222.40	17-Aug-27	05-Sep-27			0.00	0.00	0.00
CON-LEG101-LR-5370	Installation of a Flush valve [Local – 01 Segment-03]	5	14,740.00	17-Aug-27	22-Aug-27			0.00	0.00	0.00
CON-LEG101-LR-5540	Installation of Decoder cables 12 AWG between valves and controllers [	12	6,482.40	23-Aug-27	05-Sep-27			0.00	0.00	0.00
Curbs and edging		2	1,366.80	06-Sep-27	07-Sep-27			0.00	0.00	0.00
CON-LEG101-LR-4810	Installation of Curbs and edging [Local – 01 Segment-03]	2	1,366.80	06-Sep-27	07-Sep-27			0.00	0.00	0.00
Landscape		27	33,588.50	08-Sep-27	10-Oct-27			0.00	0.00	0.00
CON-LEG101-LR-4600	Site preparation for Planting Area [Local – 01 Segment-03]	9	6,717.70	08-Sep-27	18-Sep-27			0.00	0.00	0.00
CON-LEG101-LR-4670	Placing Agricutural Soil [Local – 01 Segment-03]	9	6,717.70	19-Sep-27	29-Sep-27			0.00	0.00	0.00
CON-LEG101-LR-4740	Planting Shrubs And Ground Cover [Local – 01 Segment-03]	9	20,153.10	30-Sep-27	10-Oct-27			0.00	0.00	0.00
Local – 02		63	104,341.90	05-Aug-27	18-Oct-27			0.00	0.00	0.00
Irrigation Works		53	69,386.60	05-Aug-27	06-Oct-27			0.00	0.00	0.00
Secondary Irrigation		53	69,386.60	05-Aug-27	06-Oct-27			0.00	0.00	0.00
Pipe Work		53	41,464.20	05-Aug-27	06-Oct-27			0.00	0.00	0.00
CON-LEG101-LR-4900	Excavation for Secondary Irrigation [Local – 02]	4	412.00	05-Aug-27	09-Aug-27			0.00	0.00	0.00
CON-LEG101-LR-4970	Sand bedding for Secondary Irrigation [Local – 02]	4	0.00	10-Aug-27	14-Aug-27			0.00	0.00	0.00
CON-LEG101-LR-5040	Installation of Pipe for Secondary Irrigation [Local – 02]	4	1,237.80	15-Aug-27	18-Aug-27			0.00	0.00	0.00
CON-LEG101-LR-5110	Sand Surround for Secondary Irrigation [Local – 02]	8	0.00	19-Aug-27	28-Aug-27			0.00	0.00	0.00
CON-LEG101-LR-5180	Installation of Micron Marker Magnetic Tape [Local – 02]	8	0.00	29-Aug-27	06-Sep-27			0.00	0.00	0.00
CON-LEG101-LR-5240	Backfilling to Subgrade Elevation [Local – 02]	10	412.00	07-Sep-27	18-Sep-27			0.00	0.00	0.00
CON-LEG101-LR-5440	Installation of tubing for risers connections from laterals [Local – 02]	15	39,402.40	19-Sep-27	06-Oct-27			0.00	0.00	0.00
Valves and Controller		30	27,922.40	19-Aug-27	22-Sep-27			0.00	0.00	0.00
CON-LEG101-LR-5280	Installation of Electrical Solenoid Valve [Local – 02]	5	5,025.00	19-Aug-27	24-Aug-27			0.00	0.00	0.00
CON-LEG101-LR-5320	Installation of quick coupler valve [Local – 02]	5	3,015.00	25-Aug-27	30-Aug-27			0.00	0.00	0.00
CON-LEG101-LR-5380	Installation of a Flush valve [Local – 02]	4	6,700.00	31-Aug-27	04-Sep-27			0.00	0.00	0.00
CON-LEG101-LR-5490	Install single station decoder for valve connection [Local – 02]	7	6,700.00	05-Sep-27	12-Sep-27			0.00	0.00	0.00
CON-LEG101-LR-5550	Installation of Decoder cables 12 AWG between valves and controllers [	9	6,482.40	13-Sep-27	22-Sep-27			0.00	0.00	0.00
Curbs and edging		3	1,366.80	25-Sep-27	27-Sep-27			0.00	0.00	0.00
CON-LEG101-LR-4830	Installation of Curbs and edging [Local – 02]	3	1,366.80	25-Sep-27	27-Sep-27			0.00	0.00	0.00
Landscape		18	33,588.50	28-Sep-27	18-Oct-27			0.00	0.00	0.00

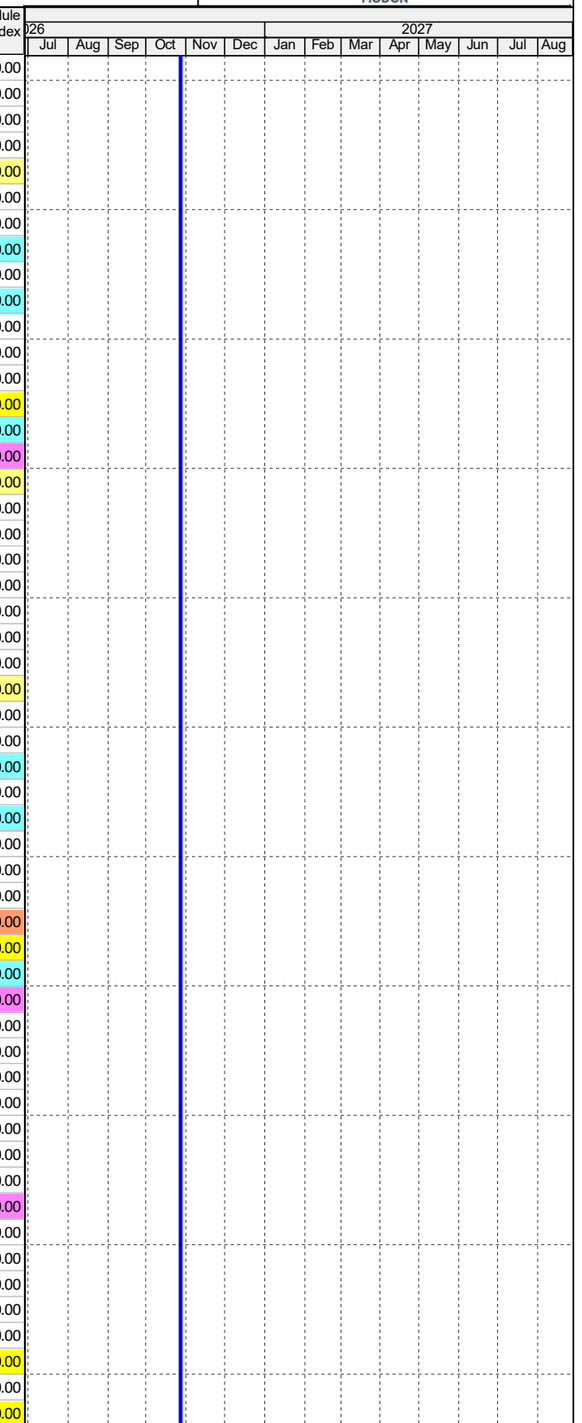


© Oracle Corporation

Activity ID	Activity Name	Original Duration	Budgeted Total Cost	BL Project Start	BL Project Finish	Actual Start	Actual Finish	Planned Value Cost	Earned Value Cost	Schedule Performance Index
CON-LEG101-LR-4610	Site preparation for Planting Area [Local – 02]	6	6,717.70	28-Sep-27	04-Oct-27			0.00	0.00	0.00
CON-LEG101-LR-4680	Placing Agricutural Soil [Local – 02]	6	6,717.70	05-Oct-27	11-Oct-27			0.00	0.00	0.00
CON-LEG101-LR-4750	Planting Shrubs And Ground Cover [Local – 02]	6	20,153.10	12-Oct-27	18-Oct-27			0.00	0.00	0.00
Local – 04		55	89,602.70	05-Aug-27	09-Oct-27			0.00	0.00	0.00
Irrigation Works		43	54,647.40	05-Aug-27	25-Sep-27			0.00	0.00	0.00
Secondary Irrigation		43	54,647.40	05-Aug-27	25-Sep-27			0.00	0.00	0.00
Pipe Work		29	41,465.00	05-Aug-27	07-Sep-27			0.00	0.00	0.00
CON-LEG101-LR-4910	Excavation for Secondary Irrigation [Local – 04]	3	412.00	05-Aug-27	08-Aug-27			0.00	0.00	0.00
CON-LEG101-LR-4980	Sand bedding for Secondary Irrigation [Local – 04]	6	0.00	09-Aug-27	15-Aug-27			0.00	0.00	0.00
CON-LEG101-LR-5050	Installation of Pipe for Secondary Irrigation [Local – 04]	8	1,237.80	16-Aug-27	24-Aug-27			0.00	0.00	0.00
CON-LEG101-LR-5120	Sand Surround for Secondary Irrigation [Local – 04]	3	0.00	25-Aug-27	28-Aug-27			0.00	0.00	0.00
CON-LEG101-LR-5190	Installation of Micron Marker Magnetic Tape [Local – 04]	5	0.00	29-Aug-27	02-Sep-27			0.00	0.00	0.00
CON-LEG101-LR-5250	Backfilling to Subgrade Elevation [Local – 04]	2	412.00	04-Sep-27	05-Sep-27			0.00	0.00	0.00
CON-LEG101-LR-5450	Installation of tubing for risers connections from laterals [Local – 04]	2	39,403.20	06-Sep-27	07-Sep-27			0.00	0.00	0.00
Valves and Controller		26	13,182.40	25-Aug-27	25-Sep-27			0.00	0.00	0.00
CON-LEG101-LR-5290	Installation of Electrical Solenoid Valve [Local – 04]	6	0.00	25-Aug-27	31-Aug-27			0.00	0.00	0.00
CON-LEG101-LR-5330	Installation of quick coupler valve [Local – 04]	6	0.00	01-Sep-27	07-Sep-27			0.00	0.00	0.00
CON-LEG101-LR-5390	Installation of a Flush valve [Local – 04]	5	6,700.00	08-Sep-27	13-Sep-27			0.00	0.00	0.00
CON-LEG101-LR-5500	Install single station decoder for valve connection [Local – 04]	7	0.00	14-Sep-27	21-Sep-27			0.00	0.00	0.00
CON-LEG101-LR-5560	Installation of Decoder cables 12 AWG between valves and controllers [	2	6,482.40	22-Sep-27	25-Sep-27			0.00	0.00	0.00
Curbs and edging		3	1,366.80	26-Sep-27	28-Sep-27			0.00	0.00	0.00
CON-LEG101-LR-4840	Installation of Curbs and edging [Local – 04]	3	1,366.80	26-Sep-27	28-Sep-27			0.00	0.00	0.00
Landscape		9	33,588.50	29-Sep-27	09-Oct-27			0.00	0.00	0.00
CON-LEG101-LR-4620	Site preparation for Planting Area [Local – 04]	3	6,717.70	29-Sep-27	02-Oct-27			0.00	0.00	0.00
CON-LEG101-LR-4690	Placing Agricutural Soil [Local – 04]	3	6,717.70	03-Oct-27	05-Oct-27			0.00	0.00	0.00
CON-LEG101-LR-4760	Planting Shrubs And Ground Cover [Local – 04]	3	20,153.10	06-Oct-27	09-Oct-27			0.00	0.00	0.00
Local – 06		56	100,322.70	05-Aug-27	10-Oct-27			0.00	0.00	0.00
Irrigation Works		41	65,367.40	05-Aug-27	21-Sep-27			0.00	0.00	0.00
Secondary Irrigation		41	65,367.40	05-Aug-27	21-Sep-27			0.00	0.00	0.00
Pipe Work		17	41,465.00	05-Aug-27	24-Aug-27			0.00	0.00	0.00
CON-LEG101-LR-4920	Excavation for Secondary Irrigation [Local – 06]	3	412.00	05-Aug-27	08-Aug-27			0.00	0.00	0.00
CON-LEG101-LR-5060	Installation of Pipe for Secondary Irrigation [Local – 06]	3	1,237.80	09-Aug-27	11-Aug-27			0.00	0.00	0.00
CON-LEG101-LR-5260	Backfilling to Subgrade Elevation [Local – 06]	3	412.00	12-Aug-27	15-Aug-27			0.00	0.00	0.00
CON-LEG101-LR-5460	Installation of tubing for risers connections from laterals [Local – 06]	8	39,403.20	16-Aug-27	24-Aug-27			0.00	0.00	0.00
Valves and Controller		24	23,902.40	25-Aug-27	21-Sep-27			0.00	0.00	0.00
CON-LEG101-LR-5300	Installation of Electrical Solenoid Valve [Local – 06]	4	4,355.00	25-Aug-27	29-Aug-27			0.00	0.00	0.00
CON-LEG101-LR-5340	Installation of quick coupler valve [Local – 06]	4	3,015.00	30-Aug-27	02-Sep-27			0.00	0.00	0.00
CON-LEG101-LR-5400	Installation of a Flush valve [Local – 06]	5	6,700.00	04-Sep-27	08-Sep-27			0.00	0.00	0.00
CON-LEG101-LR-5510	Install single station decoder for valve connection [Local – 06]	5	3,350.00	09-Sep-27	14-Sep-27			0.00	0.00	0.00
CON-LEG101-LR-5570	Installation of Decoder cables 12 AWG between valves and controllers [	6	6,482.40	15-Sep-27	21-Sep-27			0.00	0.00	0.00
Curbs and edging		3	1,366.80	22-Sep-27	26-Sep-27			0.00	0.00	0.00
CON-LEG101-LR-4850	Installation of Curbs and edging [Local – 06]	3	1,366.80	22-Sep-27	26-Sep-27			0.00	0.00	0.00
Landscape		12	33,588.50	27-Sep-27	10-Oct-27			0.00	0.00	0.00
CON-LEG101-LR-4630	Site preparation for Planting Area [Local – 06]	4	6,717.70	27-Sep-27	30-Sep-27			0.00	0.00	0.00
CON-LEG101-LR-4700	Placing Agricutural Soil [Local – 06]	4	6,717.70	02-Oct-27	05-Oct-27			0.00	0.00	0.00
CON-LEG101-LR-4770	Planting Shrubs And Ground Cover [Local – 06]	4	20,153.10	06-Oct-27	10-Oct-27			0.00	0.00	0.00
Roundabout - 01 (L01 & L04)		153	349,038.30	07-Apr-27	07-Oct-27			0.00	0.00	0.00
Irrigation Works		96	209,216.00	07-Apr-27	01-Aug-27			0.00	0.00	0.00
Secondary Irrigation		96	209,216.00	07-Apr-27	01-Aug-27			0.00	0.00	0.00
Pipe Work		96	165,867.00	07-Apr-27	01-Aug-27			0.00	0.00	0.00
CON-LEG101-RA-1120	Excavation for Secondary Irrigation [Roundabout : 01]	11	1,651.60	07-Apr-27	19-Apr-27			0.00	0.00	0.00
CON-LEG101-RA-1150	Sand bedding for Secondary Irrigation [Roundabout : 01]	11	0.00	20-Apr-27	02-May-27			0.00	0.00	0.00
CON-LEG101-RA-1180	Installation of Pipe for Secondary Irrigation [Roundabout : 01]	11	4,953.00	03-May-27	19-May-27			0.00	0.00	0.00

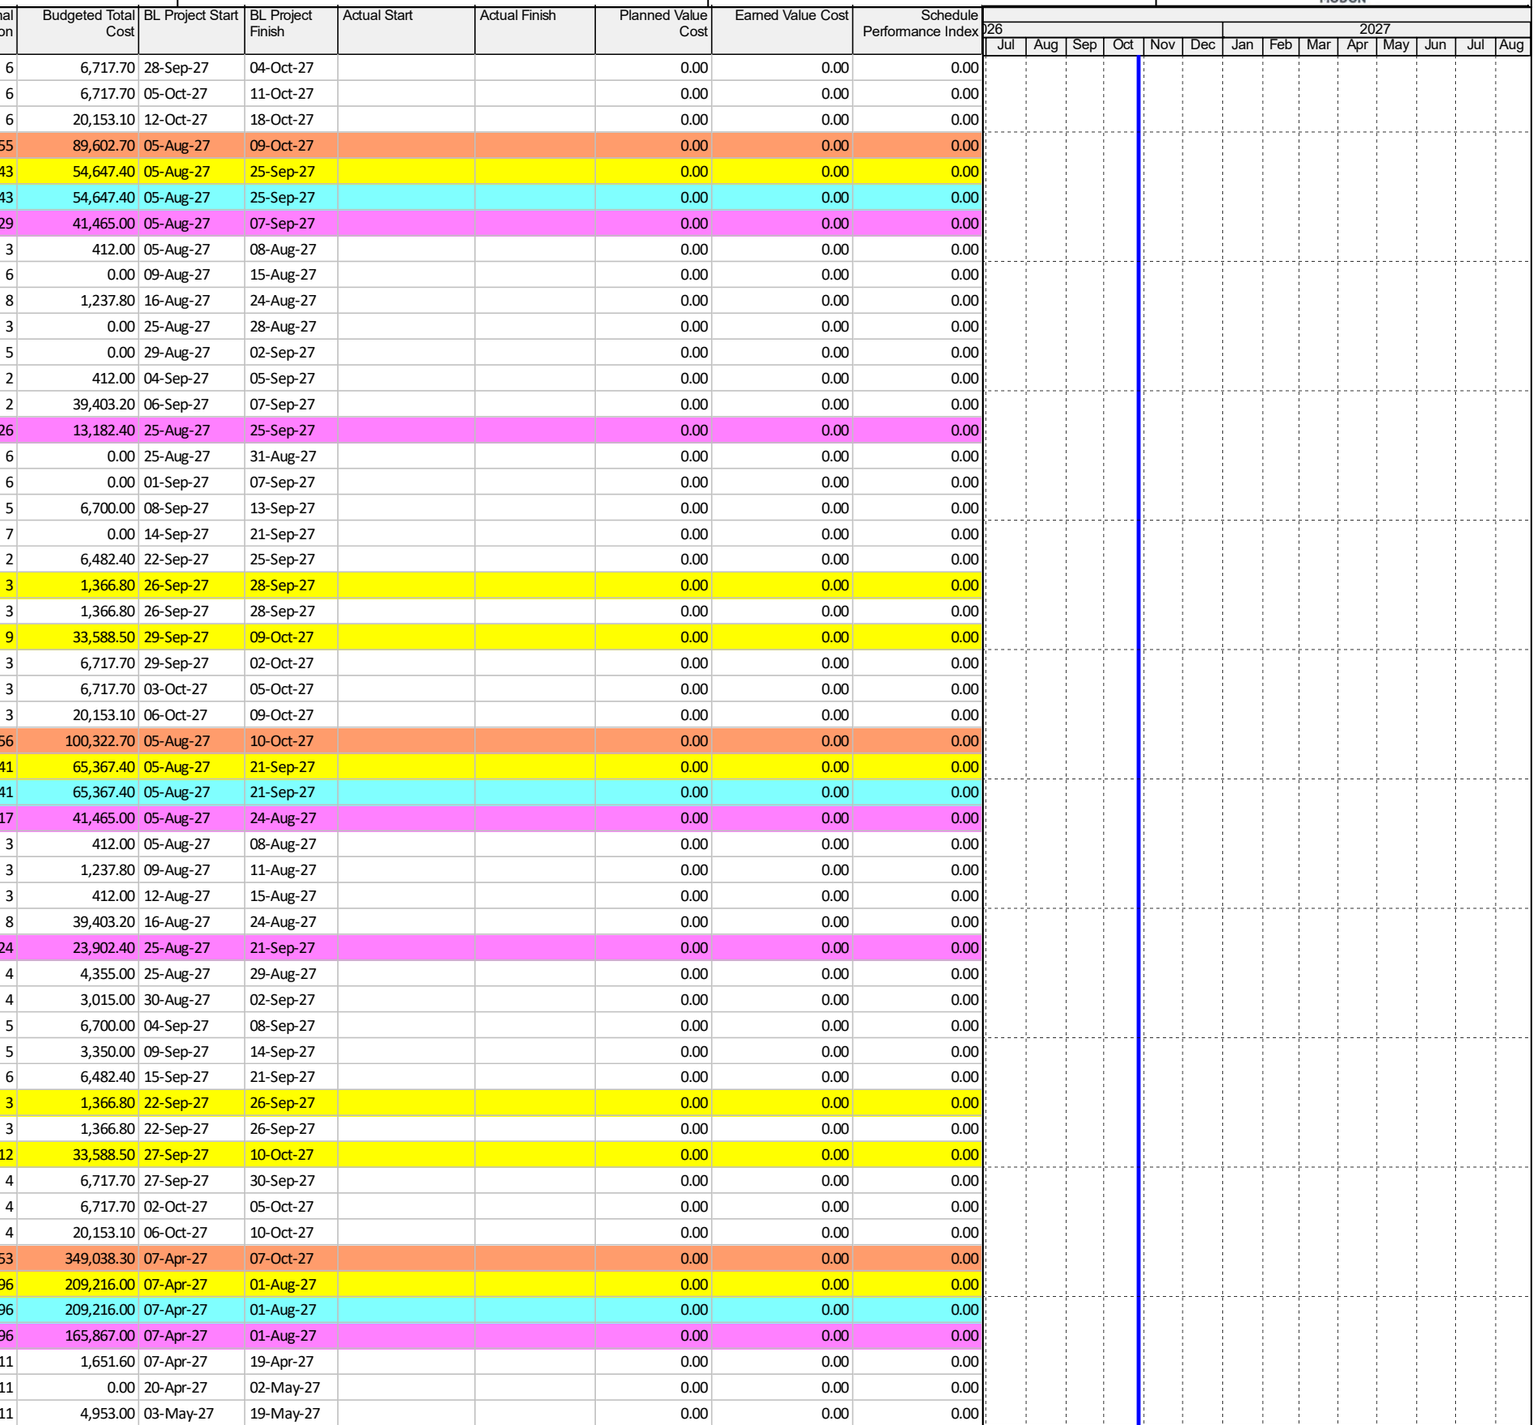


© Oracle Corporation

Activity ID	Activity Name	Original Duration	Budgeted Total Cost	BL Project Start	BL Project Finish	Actual Start	Actual Finish	Planned Value Cost	Earned Value Cost	Schedule Performance Index
CON-LEG101-RA-1210	Sand Surround for Secondary Irrigation [Roundabout : 01]	14	0.00	20-May-27	05-Jun-27			0.00	0.00	0.00
CON-LEG101-RA-1240	Installation of Micron Marker Magnetic Tape [Roundabout : 01]	14	0.00	06-Jun-27	21-Jun-27			0.00	0.00	0.00
CON-LEG101-RA-1270	Backfilling to Subgrade Elevation [Roundabout : 01]	14	1,651.60	22-Jun-27	07-Jul-27			0.00	0.00	0.00
CON-LEG101-RA-1390	Installation of tubing for risers connections from laterals [Roundabout :	21	157,610.80	08-Jul-27	01-Aug-27			0.00	0.00	0.00
Valves and Controller		49	43,349.00	20-May-27	30-Jun-27			0.00	0.00	0.00
A	Catch	14	25,929.00					0.00	0.00	0.00
CON-LEG101-RA-1300	Installation of Electrical Solenoid Valve [Roundabout : 01]	5	4,355.00	20-May-27	25-May-27			0.00	0.00	0.00
CON-LEG101-RA-1330	Installation of quick coupler valve [Roundabout : 01]	5	3,015.00	26-May-27	31-May-27			0.00	0.00	0.00
CON-LEG101-RA-1360	Installation of a Flush valve [Roundabout : 01]	11	6,700.00	01-Jun-27	13-Jun-27			0.00	0.00	0.00
CON-LEG101-RA-1420	Install single station decoder for valve connection [Roundabout : 01]	14	3,350.00	15-Jun-27	30-Jun-27			0.00	0.00	0.00
Curbs and edging		12	5,467.20	18-Jul-27	31-Jul-27			0.00	0.00	0.00
CON-LEG101-RA-1090	Installation of Curbs and edging [Roundabout : 01]	12	5,467.20	18-Jul-27	31-Jul-27			0.00	0.00	0.00
Landscape		57	134,355.10	02-Aug-27	07-Oct-27			0.00	0.00	0.00
CON-LEG101-RA-1000	Site preparation for Planting Area [Roundabout : 01]	19	26,870.80	02-Aug-27	23-Aug-27			0.00	0.00	0.00
CON-LEG101-RA-1030	Placing Agricutural Soil [Roundabout : 01]	19	26,870.80	24-Aug-27	14-Sep-27			0.00	0.00	0.00
CON-LEG101-RA-1060	Planting Shrubs And Ground Cover [Roundabout : 01]	19	80,613.50	15-Sep-27	07-Oct-27			0.00	0.00	0.00
Roundabout - 02 (L01 & L03)		108	349,038.30	14-Jun-27	18-Oct-27			0.00	0.00	0.00
Irrigation Works		96	209,216.00	14-Jun-27	04-Oct-27			0.00	0.00	0.00
Secondary Irrigation		96	209,216.00	14-Jun-27	04-Oct-27			0.00	0.00	0.00
Pipe Work		96	165,867.00	14-Jun-27	04-Oct-27			0.00	0.00	0.00
CON-LEG101-RA-1130	Excavation for Secondary Irrigation [Roundabout : 02]	11	1,651.60	14-Jun-27	26-Jun-27			0.00	0.00	0.00
CON-LEG101-RA-1160	Sand bedding for Secondary Irrigation [Roundabout : 02]	11	0.00	27-Jun-27	08-Jul-27			0.00	0.00	0.00
CON-LEG101-RA-1190	Installation of Pipe for Secondary Irrigation [Roundabout : 02]	11	4,953.00	10-Jul-27	21-Jul-27			0.00	0.00	0.00
CON-LEG101-RA-1220	Sand Surround for Secondary Irrigation [Roundabout : 02]	14	0.00	22-Jul-27	07-Aug-27			0.00	0.00	0.00
CON-LEG101-RA-1250	Installation of Micron Marker Magnetic Tape [Roundabout : 02]	14	0.00	08-Aug-27	23-Aug-27			0.00	0.00	0.00
CON-LEG101-RA-1280	Backfilling to Subgrade Elevation [Roundabout : 02]	14	1,651.60	24-Aug-27	08-Sep-27			0.00	0.00	0.00
CON-LEG101-RA-1400	Installation of tubing for risers connections from laterals [Roundabout :	21	157,610.80	09-Sep-27	04-Oct-27			0.00	0.00	0.00
Valves and Controller		42	43,349.00	22-Jul-27	08-Sep-27			0.00	0.00	0.00
CON-LEG101-RA-1460	Installation of Decoder cables 12 AWG between valves and controllers [	14	25,929.00	24-Aug-27	08-Sep-27			0.00	0.00	0.00
CON-LEG101-RA-1310	Installation of Electrical Solenoid Valve [Roundabout : 02]	5	4,355.00	22-Jul-27	27-Jul-27			0.00	0.00	0.00
CON-LEG101-RA-1340	Installation of quick coupler valve [Roundabout : 02]	5	3,015.00	28-Jul-27	02-Aug-27			0.00	0.00	0.00
CON-LEG101-RA-1370	Installation of a Flush valve [Roundabout : 02]	11	6,700.00	03-Aug-27	15-Aug-27			0.00	0.00	0.00
CON-LEG101-RA-1430	Install single station decoder for valve connection [Roundabout : 02]	7	3,350.00	16-Aug-27	23-Aug-27			0.00	0.00	0.00
Curbs and edging		3	5,467.20	09-Sep-27	12-Sep-27			0.00	0.00	0.00
CON-LEG101-RA-1100	Installation of Curbs and edging [Roundabout : 02]	3	5,467.20	09-Sep-27	12-Sep-27			0.00	0.00	0.00
Landscape		30	134,355.10	13-Sep-27	18-Oct-27			0.00	0.00	0.00
CON-LEG101-RA-1010	Site preparation for Planting Area [Roundabout : 02]	10	26,870.80	13-Sep-27	25-Sep-27			0.00	0.00	0.00
CON-LEG101-RA-1040	Placing Agricutural Soil [Roundabout : 02]	10	26,870.80	26-Sep-27	06-Oct-27			0.00	0.00	0.00
CON-LEG101-RA-1070	Planting Shrubs And Ground Cover [Roundabout : 02]	10	80,613.50	07-Oct-27	18-Oct-27			0.00	0.00	0.00
Roundabout - 03 (L03 & L05)		97	349,038.30	27-Jun-27	18-Oct-27			0.00	0.00	0.00
Irrigation Works		84	209,216.00	27-Jun-27	03-Oct-27			0.00	0.00	0.00
Secondary Irrigation		84	209,216.00	27-Jun-27	03-Oct-27			0.00	0.00	0.00
Pipe Work		84	165,867.00	27-Jun-27	03-Oct-27			0.00	0.00	0.00
CON-LEG101-RA-1140	Excavation for Secondary Irrigation [Roundabout : 03]	11	1,651.60	27-Jun-27	08-Jul-27			0.00	0.00	0.00
CON-LEG101-RA-1170	Sand bedding for Secondary Irrigation [Roundabout : 03]	10	0.00	10-Jul-27	20-Jul-27			0.00	0.00	0.00
CON-LEG101-RA-1200	Installation of Pipe for Secondary Irrigation [Roundabout : 03]	11	4,953.00	21-Jul-27	02-Aug-27			0.00	0.00	0.00
CON-LEG101-RA-1230	Sand Surround for Secondary Irrigation [Roundabout : 03]	11	0.00	03-Aug-27	15-Aug-27			0.00	0.00	0.00
CON-LEG101-RA-1260	Installation of Micron Marker Magnetic Tape [Roundabout : 03]	11	0.00	16-Aug-27	28-Aug-27			0.00	0.00	0.00
CON-LEG101-RA-1290	Backfilling to Subgrade Elevation [Roundabout : 03]	11	1,651.60	29-Aug-27	09-Sep-27			0.00	0.00	0.00
CON-LEG101-RA-1410	Installation of tubing for risers connections from laterals [Roundabout :	19	157,610.80	11-Sep-27	03-Oct-27			0.00	0.00	0.00
Valves and Controller		42	43,349.00	03-Aug-27	20-Sep-27			0.00	0.00	0.00
CON-LEG101-RA-1470	Installation of Decoder cables 12 AWG between valves and controllers [	14	25,929.00	05-Sep-27	20-Sep-27			0.00	0.00	0.00
CON-LEG101-RA-1320	Installation of Electrical Solenoid Valve [Roundabout : 03]	5	4,355.00	03-Aug-27	08-Aug-27			0.00	0.00	0.00

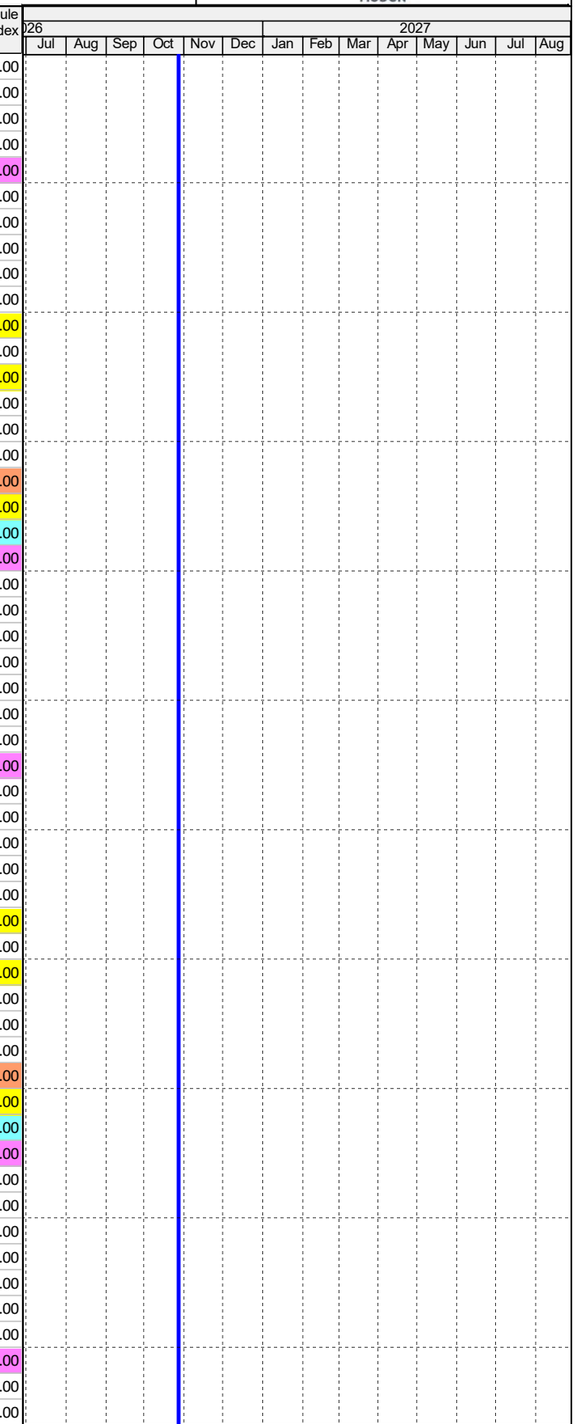


© Oracle Corporation

Activity ID	Activity Name	Original Duration	Budgeted Total Cost	BL Project Start	BL Project Finish	Actual Start	Actual Finish	Planned Value Cost	Earned Value Cost	Schedule Performance Index
CON-LEG101-RA-1350	Installation of quick coupler valve [Roundabout : 03]	5	3,015.00	09-Aug-27	14-Aug-27			0.00	0.00	0.00
CON-LEG101-RA-1380	Installation of a Flush valve [Roundabout : 03]	11	6,700.00	15-Aug-27	26-Aug-27			0.00	0.00	0.00
CON-LEG101-RA-1440	Install single station decoder for valve connection [Roundabout : 03]	7	3,350.00	28-Aug-27	04-Sep-27			0.00	0.00	0.00
Curbs and edging		3	5,467.20	21-Sep-27	25-Sep-27			0.00	0.00	0.00
CON-LEG101-RA-1110	Installation of Curbs and edging [Roundabout : 03]	3	5,467.20	21-Sep-27	25-Sep-27			0.00	0.00	0.00
Landscape		20	134,355.10	26-Sep-27	18-Oct-27			0.00	0.00	0.00
CON-LEG101-RA-1020	Site preparation for Planting Area [Roundabout : 03]	7	26,870.80	26-Sep-27	03-Oct-27			0.00	0.00	0.00
CON-LEG101-RA-1050	Placing Agricutural Soil [Roundabout : 03]	6	26,870.80	04-Oct-27	10-Oct-27			0.00	0.00	0.00
CON-LEG101-RA-1080	Planting Shrubs And Ground Cover [Roundabout : 03]	7	80,613.50	11-Oct-27	18-Oct-27			0.00	0.00	0.00
Testing & Commissioning		173	8,677,691.20	04-Aug-27	26-Oct-27	15-Jun-26		0.00	5,426,563.31	0.00
CON-LEG101-TC-1000	Test for Telecommunications Work	6	341,181.00	06-Oct-27	12-Oct-27	01-Aug-26		0.00	102,354.30	0.00
CON-LEG101-TC-1010	Test for Electrical Network	8	418,189.00	11-Sep-27	19-Sep-27	01-Aug-26		0.00	167,275.60	0.00
CON-LEG101-TC-1020	Test for Public Water Utility Distribution	8	494,212.00	14-Aug-27	22-Aug-27	15-Jun-26		0.00	395,369.60	0.00
CON-LEG101-TC-1030	Test for TSE Network	7	581,275.00	20-Sep-27	28-Sep-27	15-Jun-26		0.00	465,020.00	0.00
CON-LEG101-TC-1040	Test for Sanitary Sewerage	8	568,550.00	14-Aug-27	22-Aug-27	15-Jun-26		0.00	426,412.50	0.00
CON-LEG101-TC-1050	Test for Stormwater Utilities	8	1,041,566.00	23-Aug-27	31-Aug-27	15-Jun-26		0.00	781,174.50	0.00
CON-LEG101-TC-1060	Test for Bridge Work	8	345,044.70	01-Sep-27	09-Sep-27	15-Jun-26		0.00	224,279.06	0.00
CON-LEG101-TC-1070	Test for CCTV feeding system and GSM	6	249,750.00	13-Oct-27	19-Oct-27	01-Aug-26		0.00	99,900.00	0.00
CON-LEG101-TC-1080	Test for Fence & Gate	6	1,179,417.00	19-Oct-27	25-Oct-27	15-Jun-26		0.00	707,650.20	0.00
CON-LEG101-TC-1090	Test for Irrigation and Landscape	7	305,575.00	19-Oct-27	26-Oct-27			0.00	0.00	0.00
CON-LEG101-TC-1100	Test for Road Lighting	6	477,615.00	29-Sep-27	05-Oct-27	01-Aug-26		0.00	191,046.00	0.00
CON-LEG101-TC-1110	Test for Road Works	8	2,658,716.50	04-Aug-27	12-Aug-27	01-Aug-26		0.00	1,861,101.55	0.00
CON-LEG101-TC-1120	Test for Earthing System	6	16,600.00	20-Oct-27	26-Oct-27	01-Aug-26		0.00	4,980.00	0.00
Project Close-out		146	0.00	14-Aug-27	18-Nov-27			0.00	0.00	0.00
As-Built DWGs		136	0.00	14-Aug-27	07-Nov-27			0.00	0.00	0.00
As-Built DWGs Submittal		131	0.00	14-Aug-27	01-Nov-27			0.00	0.00	0.00
CON-LEG101-ABS-1000	As-Built DWGs Submittal for Telecommunications Work	12	0.00	13-Oct-27	26-Oct-27			0.00	0.00	0.00
CON-LEG101-ABS-1010	As-Built DWGs Submittal for Electrical Network	12	0.00	30-Sep-27	13-Oct-27			0.00	0.00	0.00
CON-LEG101-ABS-1020	As-Built DWGs Submittal for Public Water Utility Distribution	12	0.00	23-Aug-27	05-Sep-27			0.00	0.00	0.00
CON-LEG101-ABS-1030	As-Built DWGs Submittal for TSE Network	12	0.00	29-Sep-27	12-Oct-27			0.00	0.00	0.00
CON-LEG101-ABS-1040	As-Built DWGs Submittal for Sanitary Sewerage	12	0.00	15-Sep-27	29-Sep-27			0.00	0.00	0.00
CON-LEG101-ABS-1050	As-Built DWGs Submittal for Stormwater Utilities	12	0.00	01-Sep-27	14-Sep-27			0.00	0.00	0.00
CON-LEG101-ABS-1060	As-Built DWGs Submittal for Bridge Work	12	0.00	11-Sep-27	25-Sep-27			0.00	0.00	0.00
CON-LEG101-ABS-1070	As-Built DWGs Submittal for CCTV feeding system and GSM	8	0.00	20-Oct-27	28-Oct-27			0.00	0.00	0.00
CON-LEG101-ABS-1080	As-Built DWGs Submittal for Fence & Gate	6	0.00	26-Oct-27	01-Nov-27			0.00	0.00	0.00
CON-LEG101-ABS-1090	As-Built DWGs Submittal for Irrigation and Landscape	5	0.00	27-Oct-27	01-Nov-27			0.00	0.00	0.00
CON-LEG101-ABS-1100	As-Built DWGs Submittal for Road Lighting	12	0.00	06-Oct-27	19-Oct-27			0.00	0.00	0.00
CON-LEG101-ABS-1110	As-Built DWGs Submittal for Road Works	12	0.00	14-Aug-27	26-Aug-27			0.00	0.00	0.00
CON-LEG101-ABS-1120	As-Built DWGs Submittal for Earthing System	5	0.00	27-Oct-27	01-Nov-27			0.00	0.00	0.00
As-Built DWGs Approval		130	0.00	28-Aug-27	07-Nov-27			0.00	0.00	0.00
CON-LEG101-ABA-1000	As- Built DWGs Approval for Telecommunications Work	8	0.00	27-Oct-27	04-Nov-27			0.00	0.00	0.00
CON-LEG101-ABA-1010	As- Built DWGs Approval for Electrical Network	10	0.00	25-Oct-27	04-Nov-27			0.00	0.00	0.00
CON-LEG101-ABA-1020	As- Built DWGs Approval for Public Water Utility Distribution	10	0.00	08-Sep-27	19-Sep-27			0.00	0.00	0.00
CON-LEG101-ABA-1030	As- Built DWGs Approval for TSE Network	10	0.00	13-Oct-27	24-Oct-27			0.00	0.00	0.00
CON-LEG101-ABA-1040	As- Built DWGs Approval for Sanitary Sewerage	10	0.00	25-Oct-27	04-Nov-27			0.00	0.00	0.00
CON-LEG101-ABA-1050	As- Built DWGs Approval for Stormwater Utilities	10	0.00	20-Sep-27	02-Oct-27			0.00	0.00	0.00
CON-LEG101-ABA-1060	As- Built DWGs Approval for Bridge Work	10	0.00	03-Oct-27	13-Oct-27			0.00	0.00	0.00
CON-LEG101-ABA-1070	As- Built DWGs Approval for CCTV feeding system and GSM	5	0.00	30-Oct-27	03-Nov-27			0.00	0.00	0.00
CON-LEG101-ABA-1080	As- Built DWGs Approval for Fence & Gate	5	0.00	02-Nov-27	07-Nov-27			0.00	0.00	0.00
CON-LEG101-ABA-1090	As- Built DWGs Approval for Irrigation and Landscape	5	0.00	02-Nov-27	07-Nov-27			0.00	0.00	0.00
CON-LEG101-ABA-1100	As- Built DWGs Approval for Road Lighting	10	0.00	20-Oct-27	31-Oct-27			0.00	0.00	0.00
CON-LEG101-ABA-1110	As- Built DWGs Approval for Road Works	10	0.00	28-Aug-27	07-Sep-27			0.00	0.00	0.00

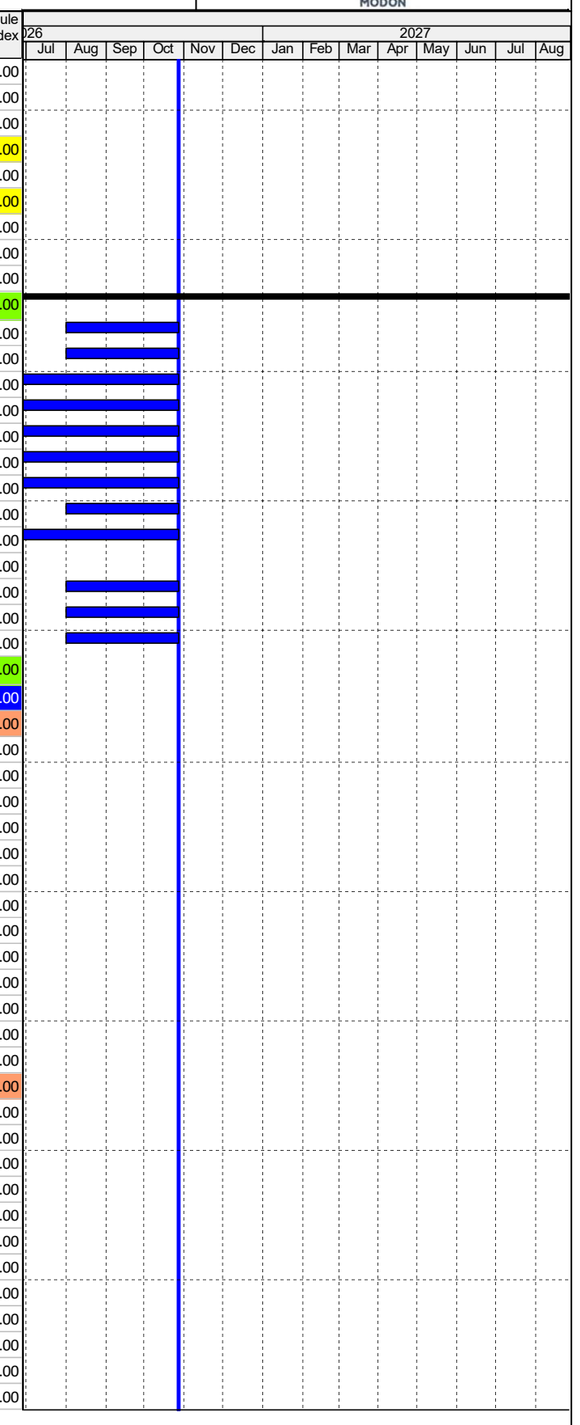

© Oracle Corporation

Activity ID	Activity Name	Original Duration	Budgeted Total Cost	BL Project Start	BL Project Finish	Actual Start	Actual Finish	Planned Value Cost	Earned Value Cost	Schedule Performance Index
CON-LEG101-ABA-1120	As- Built DWGs Approval for Earthing System	5	0.00	02-Nov-27	07-Nov-27			0.00	0.00	0.00
Demobilization		10	0.00	08-Nov-27	18-Nov-27			0.00	0.00	0.00
CON-LEG101-DM-1000	Demobilization of Manpower	5	0.00	08-Nov-27	13-Nov-27			0.00	0.00	0.00
CON-LEG101-DM-1010	Removal of Equipment from Site	5	0.00	08-Nov-27	13-Nov-27			0.00	0.00	0.00
CON-LEG101-DM-1020	Site Clean Up	5	0.00	08-Nov-27	13-Nov-27			0.00	0.00	0.00
CON-LEG101-DM-1030	Removal of Site Offices and Structures	5	0.00	08-Nov-27	13-Nov-27			0.00	0.00	0.00
CON-LEG101-DM-1040	Restoration of Ground Surfaces	5	0.00	14-Nov-27	18-Nov-27			0.00	0.00	0.00



© Oracle Corporation
