

Activity ID	Activity Name	Original Duration	BL Project Start	BL Project Finish	Start	Finish
20 READY BUILT FACTORIES 900 m2 IN HAIL		162	14-Feb-26	29-Nov-26	01-Apr-26 A	11-Nov-26
PROJECT MILESTONES		11	09-Apr-26	11-Oct-26	28-Sep-26	10-Oct-26
CONTRACTUAL MILESTONES		0	09-Apr-26	09-Apr-26	28-Sep-26	28-Sep-26
HAL-PMS-MMS-0060	Completion of Engineering and Materials	0		09-Apr-26		28-Sep-26
DISCIPLINE MILESTONES		1	14-Jul-26	11-Oct-26	08-Oct-26	10-Oct-26
900 SQM FACTORIES		0	14-Jul-26	14-Jul-26	10-Oct-26	10-Oct-26
HAL-PMS-DMS-2310	Completion of Civil works	0		14-Jul-26		10-Oct-26
SITE INFRASTRUCTURE		0	11-Oct-26	11-Oct-26	08-Oct-26	08-Oct-26
HAL-PMS-DMS-2460	Completion of Environmentall works	0		11-Oct-26		08-Oct-26
PROCUREMENT (27%)		99	14-Feb-26	18-Aug-26	03-Jun-26 A	01-Nov-26
SHORT LEAD MATERIALS		99	14-Feb-26	18-Aug-26	03-Jun-26 A	01-Nov-26
ARCHITECTURAL		10	14-Feb-26	17-Jun-26	22-Sep-26 A	11-Oct-26
MANUFACTURING		10	14-Feb-26	01-Jun-26	22-Sep-26 A	03-Oct-26
HAL-E-MF-A-1750	Steel fence and gates	5	14-Feb-26	23-May-26	22-Sep-26 A	03-Oct-26
HAL-P-MF-A-1760	Identification sign; ID01 & ID02	5	19-Feb-26	01-Jun-26	22-Sep-26 A	03-Oct-26
DELIVERY		7	23-May-26	09-Jun-26	04-Oct-26	11-Oct-26
HAL-P-DL-A-1750	Steel fence and gates	7	23-May-26	03-Jun-26	04-Oct-26	11-Oct-26
HAL-P-DL-A-1760	Identification sign; ID01 & ID02	1	01-Jun-26	09-Jun-26	04-Oct-26	04-Oct-26
STAGING TIME		1	09-Jun-26	17-Jun-26	05-Oct-26	05-Oct-26
HAL-P-ST-A-1760	Identification sign; ID01 & ID02	1	09-Jun-26	17-Jun-26	05-Oct-26	05-Oct-26
ELECTRICAL		86	08-Mar-26	02-Jul-26	03-Jun-26 A	17-Oct-26
MANUFACTURING		30	08-Mar-26	16-Jun-26	03-Jun-26 A	30-Sep-26
HAL-P-MF-E-330	Wall mounted, duplex, telephone and data outlet	30	08-Mar-26	16-Jun-26	03-Jun-26 A	30-Sep-26
DELIVERY		7	16-Jun-26	24-Jun-26	01-Oct-26	08-Oct-26
HAL-P-DL-E-330	Wall mounted, duplex, telephone and data outlet	7	16-Jun-26	24-Jun-26	01-Oct-26	08-Oct-26
STAGING TIME		7	24-Jun-26	02-Jul-26	10-Oct-26	17-Oct-26
HAL-P-ST-E-330	Wall mounted, duplex, telephone and data outlet	7	24-Jun-26	02-Jul-26	10-Oct-26	17-Oct-26
EXTERNAL		30	11-Mar-26	18-Aug-26	28-Sep-26	01-Nov-26
PO ISSUE		5	11-Mar-26	21-Mar-26	28-Sep-26	03-Oct-26
HAL-P-PO-EX-100	Road markings	5	11-Mar-26	21-Mar-26	28-Sep-26	03-Oct-26
MANUFACTURING		25	21-Mar-26	07-Jul-26	04-Oct-26	01-Nov-26
HAL-P-MF-EX-100	Road markings	25	21-Mar-26	07-Jul-26	04-Oct-26	01-Nov-26
STAGING TIME		7	10-Aug-26	18-Aug-26	28-Sep-26	05-Oct-26
HAL-P-ST-EX-80	Asphaltworks	7	10-Aug-26	18-Aug-26	28-Sep-26	05-Oct-26
CONSTRUCTION (60%)		122	16-Jul-26	26-Nov-26	01-Apr-26 A	11-Nov-26
RBF 900 SQM FACTORIES		122	16-Jul-26	26-Nov-26	01-Apr-26 A	04-Nov-26
BLOCK B		68	30-Jul-26	25-Oct-26	17-Jun-26 A	04-Nov-26
ARCHITECTURAL		28	30-Jul-26	05-Sep-26	25-Aug-26 A	04-Nov-26
WALL FINISHES		7	30-Jul-26	08-Aug-26	25-Aug-26 A	21-Oct-26
HAL-C-B-A-680	Paint to Plaster (Primer, Putty & First Coat)	7	30-Jul-26	08-Aug-26	25-Aug-26 A	21-Oct-26
FLOOR FINISHES		7	27-Aug-26	05-Sep-26	24-Sep-26 A	29-Sep-26
HAL-C-B-A-850	Epoxy paint	7	27-Aug-26	05-Sep-26	24-Sep-26 A	29-Sep-26
METAL WORKS		5	09-Aug-26	15-Aug-26	05-Sep-26 A	04-Nov-26
HAL-C-B-A-760	Aluminium composite panel	5	09-Aug-26	15-Aug-26	05-Sep-26 A	04-Nov-26
ELECTRICAL		68	08-Aug-26	25-Oct-26	17-Jun-26 A	18-Oct-26
SECOND STAGE		68	08-Aug-26	25-Oct-26	17-Jun-26 A	18-Oct-26
HAL-C-B-E-720	Installation of CCTV System	7	17-Oct-26	25-Oct-26	17-Jun-26 A	10-Oct-26
HAL-C-B-E-503	Installation of Access Control System	4	28-Sep-26	03-Oct-26	17-Jun-26 A	29-Sep-26
HAL-C-B-E-443	Installation of Telephone Cabinet	2	17-Oct-26	19-Oct-26	13-Aug-26 A	18-Oct-26
HAL-C-B-E-730	Installation of Solar power plant	7	08-Aug-26	16-Aug-26	22-Aug-26 A	29-Sep-26
HAL-C-B-E-403	Installation of Wiring Devices	4	08-Aug-26	12-Aug-26	05-Sep-26 A	28-Sep-26

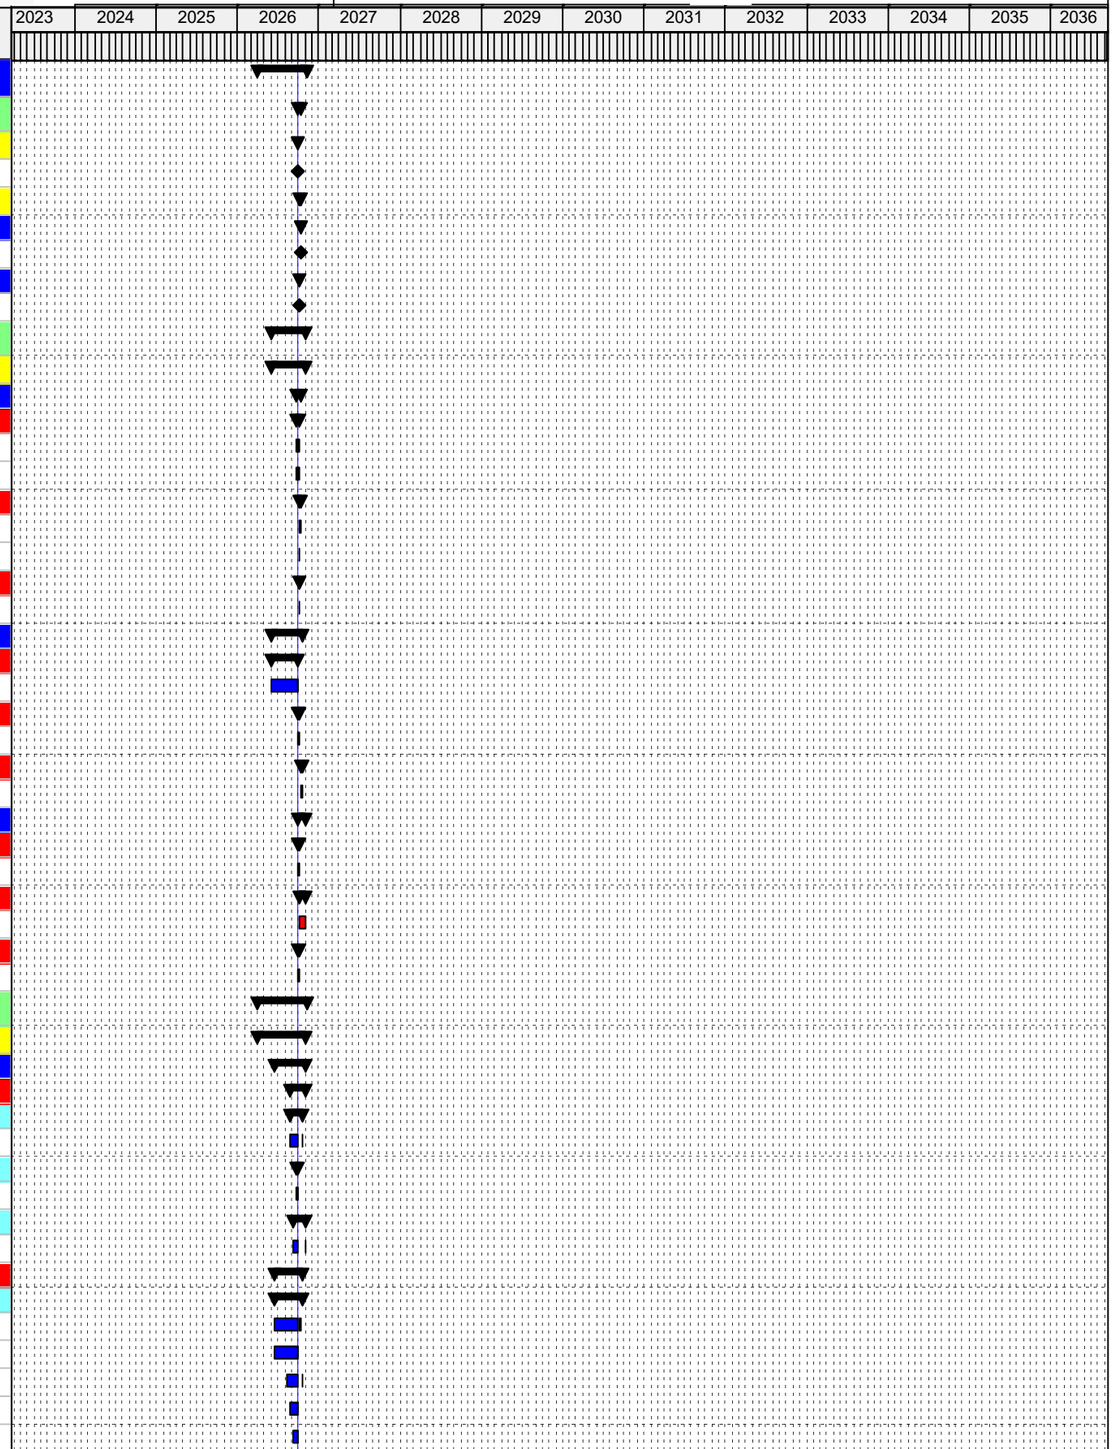

Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary

Date	Revision	Checked	Approved
28-Sep-26	Weekly Report#038		


Activity ID	Activity Name	Original Duration	BL Project Start	BL Project Finish	Start	Finish
HAL-C-B-E-433	Installation of Disconnect Switches	2	12-Aug-26	15-Aug-26	05-Sep-26 A	28-Sep-26
HAL-C-B-E-483	Installation of PP-AC panel	2	14-Oct-26	17-Oct-26	05-Sep-26 A	07-Oct-26
HAL-C-B-E-423	Installation of Main Distribution Board	2	10-Oct-26	12-Oct-26	16-Sep-26 A	07-Oct-26
HAL-C-B-E-353	Installation of Fire Alarm Control Panel	4	15-Sep-26	20-Sep-26	24-Sep-26 A	01-Oct-26
HAL-C-B-E-363	Installation of Fire Detectors & Accessories	4	20-Sep-26	26-Sep-26	24-Sep-26 A	05-Oct-26
HAL-C-B-E-383	Installation of Lighting fixtures	4	05-Oct-26	10-Oct-26	24-Sep-26 A	06-Oct-26
HAL-C-B-E-513	Monitor Modules for Fire Alarm	2	03-Oct-26	05-Oct-26	24-Sep-26 A	30-Sep-26
HAL-C-B-E-523	Line Isolator Modules for Fire Alarm	2	05-Oct-26	07-Oct-26	24-Sep-26 A	05-Oct-26
HAL-C-B-E-533	Firewarning flash light with sounder; wall mounted, Weather pr	2	07-Oct-26	10-Oct-26	24-Sep-26 A	07-Oct-26
BLOCK C		63	29-Jul-26	10-Nov-26	01-Apr-26 A	18-Oct-26
ARCHITECTURAL		32	29-Jul-26	12-Sep-26	22-Jul-26 A	18-Oct-26
WALL FINISHES		7	06-Aug-26	15-Aug-26	22-Jul-26 A	29-Sep-26
HAL-C-C-A-1500	Paint to Plaster (Primer, Putty & First Coat)	7	06-Aug-26	15-Aug-26	22-Jul-26 A	29-Sep-26
CIELING FINISHES		5	29-Jul-26	04-Aug-26	31-Aug-26 A	28-Sep-26
HAL-C-C-A-1510	Installation of Ceiling Gypsum Board	5	29-Jul-26	04-Aug-26	31-Aug-26 A	28-Sep-26
FLOOR FINISHES		7	03-Sep-26	12-Sep-26	03-Sep-26 A	18-Oct-26
HAL-C-C-A-1670	Epoxy paint	7	03-Sep-26	12-Sep-26	03-Sep-26 A	18-Oct-26
METAL WORKS		15	11-Aug-26	24-Aug-26	29-Jul-26 A	06-Oct-26
HAL-C-C-A-1580	Aluminium composite panel	5	16-Aug-26	22-Aug-26	29-Jul-26 A	04-Oct-26
HAL-C-C-A-1660	Steel railing works	4	11-Aug-26	16-Aug-26	29-Sep-26	03-Oct-26
HAL-C-C-A-1570	Galvanised Steel Gratings	2	22-Aug-26	24-Aug-26	04-Oct-26	06-Oct-26
ELECTRICAL		63	20-Sep-26	10-Nov-26	01-Apr-26 A	08-Oct-26
FIRST STAGE		24	24-Oct-26	02-Nov-26	01-Apr-26 A	07-Oct-26
HAL-C-C-E-803	Installation of Earthing and Grounding	4	28-Oct-26	02-Nov-26	01-Apr-26 A	07-Oct-26
HAL-C-C-E-913	Installation of LV Cables	2	24-Oct-26	28-Oct-26	05-Sep-26 A	06-Oct-26
SECOND STAGE		63	20-Sep-26	10-Nov-26	17-Jun-26 A	08-Oct-26
HAL-C-C-E-1340	Installation of CCTV System	2	21-Oct-26	29-Oct-26	17-Jun-26 A	07-Oct-26
HAL-C-C-E-963	Installation of Access Control System	2	24-Oct-26	28-Oct-26	17-Jun-26 A	08-Oct-26
HAL-C-C-E-903	Installation of Telephone Cabinet	2	21-Oct-26	24-Oct-26	29-Jul-26 A	07-Oct-26
HAL-C-C-E-1350	Installation of Solar power plant	7	02-Nov-26	10-Nov-26	12-Aug-26 A	29-Sep-26
HAL-C-C-E-943	Installation of PP-AC panel	2	19-Oct-26	21-Oct-26	01-Sep-26 A	06-Oct-26
HAL-C-C-E-883	Installation of Main Distribution Board	2	14-Oct-26	17-Oct-26	03-Sep-26 A	06-Oct-26
HAL-C-C-E-843	Installation of Lighting fixtures	4	10-Oct-26	14-Oct-26	10-Sep-26 A	05-Oct-26
HAL-C-C-E-823	Installation of Fire Detectors & Accessories	4	26-Sep-26	30-Sep-26	16-Sep-26 A	05-Oct-26
HAL-C-C-E-973	Monitor Modules for Fire Alarm	2	28-Oct-26	31-Oct-26	22-Sep-26 A	08-Oct-26
HAL-C-C-E-813	Installation of Fire Alarm Control Panel	4	20-Sep-26	26-Sep-26	24-Sep-26 A	05-Oct-26
HAL-C-C-E-983	Line Isolator Modules for Fire Alarm	2	31-Oct-26	02-Nov-26	24-Sep-26 A	08-Oct-26
BLOCK A		111	16-Jul-26	18-Nov-26	17-Jun-26 A	12-Oct-26
ARCHITECTURAL		25	16-Jul-26	04-Oct-26	14-Sep-26 A	12-Oct-26
WALL FINISHES		7	25-Aug-26	02-Sep-26	15-Sep-26 A	03-Oct-26
HAL-C-A-A-1090	Paint to Plaster (Primer, Putty & First Coat)	7	25-Aug-26	02-Sep-26	15-Sep-26 A	03-Oct-26
CIELING FINISHES		5	17-Aug-26	23-Aug-26	17-Sep-26 A	01-Oct-26
HAL-C-A-A-1100	Installation of Ceiling Gypsum Board	5	17-Aug-26	23-Aug-26	17-Sep-26 A	01-Oct-26
FLOOR FINISHES		9	25-Aug-26	04-Oct-26	24-Sep-26 A	10-Oct-26
HAL-C-A-A-1240	Granite strip	2	25-Aug-26	27-Aug-26	24-Sep-26 A	03-Oct-26
HAL-C-A-A-1260	Epoxy paint	7	26-Sep-26	04-Oct-26	24-Sep-26 A	10-Oct-26
DOORS & WINDOWS		3	16-Jul-26	20-Jul-26	24-Sep-26 A	28-Sep-26
HAL-C-A-A-1120	Supply and install (D4) 800*2200 mm single leaf aluminum dc	1	16-Jul-26	18-Jul-26	24-Sep-26 A	28-Sep-26
HAL-C-A-A-1130	Supply and install (D7) 1000*2200 mm single leaf aluminum c	1	18-Jul-26	19-Jul-26	24-Sep-26 A	28-Sep-26
HAL-C-A-A-1350	Supply and install (D3) 1000*2200 mm single leaf aluminum c	1	19-Jul-26	20-Jul-26	24-Sep-26 A	28-Sep-26
METAL WORKS		20	30-Aug-26	12-Sep-26	14-Sep-26 A	11-Oct-26

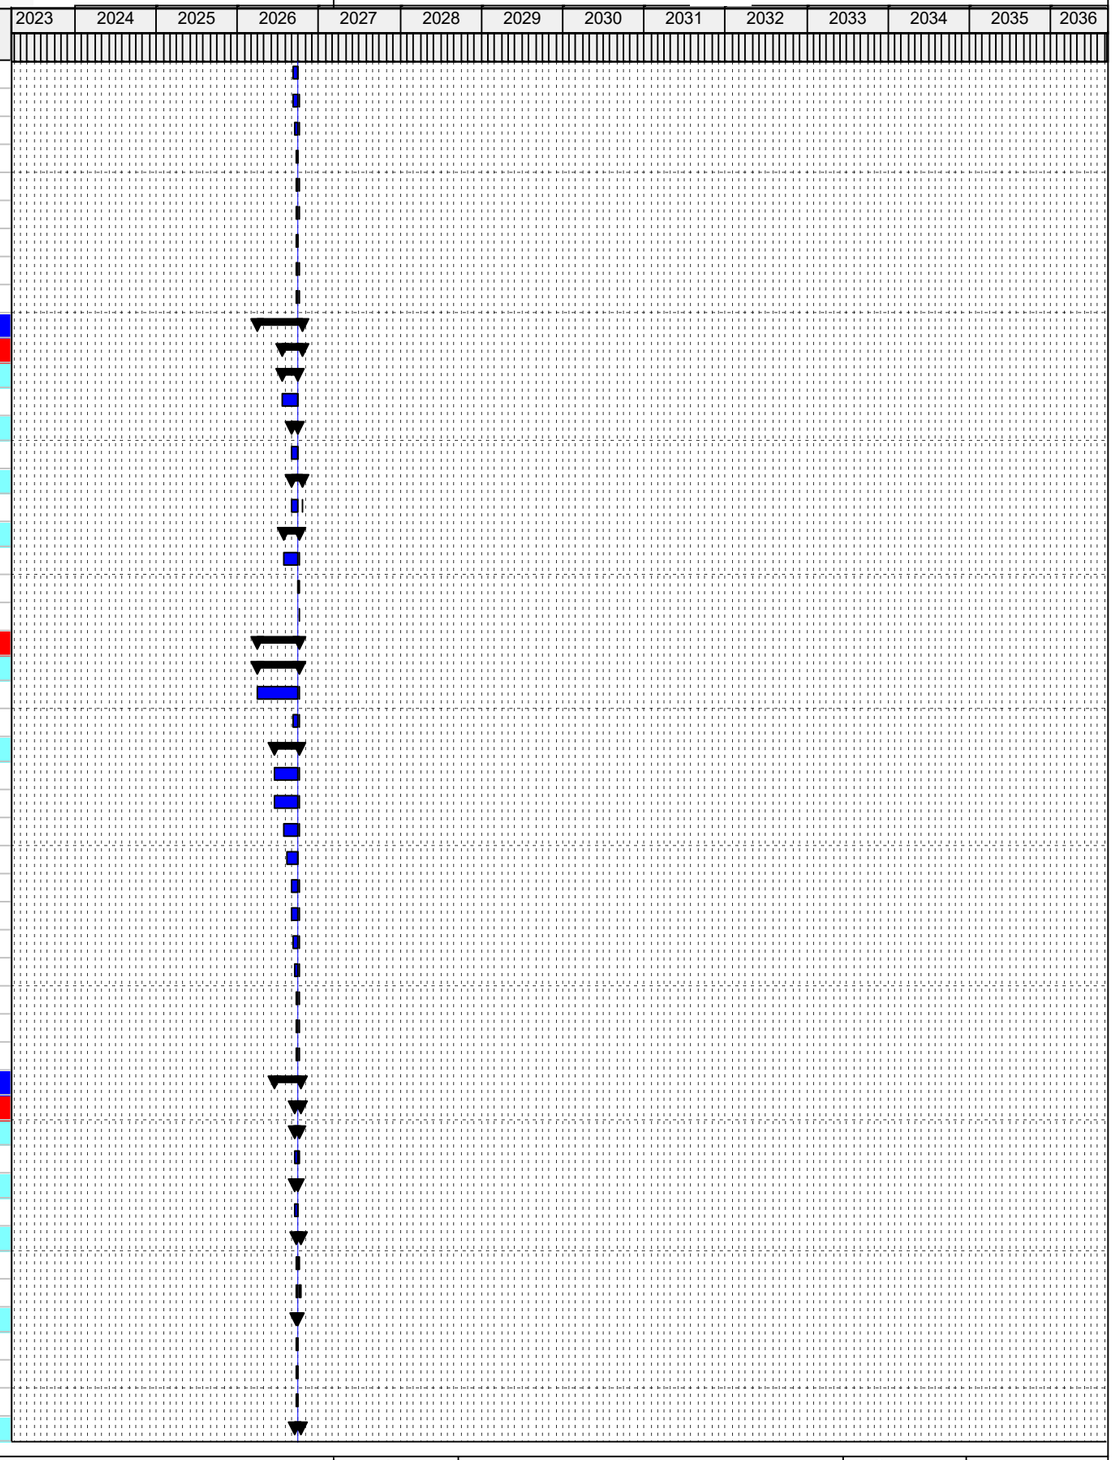

Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary

Date	Revision	Checked	Approved
28-Sep-26	Weekly Report#038		


Activity ID	Activity Name	Original Duration	BL Project Start	BL Project Finish	Start	Finish
HAL-C-A-A-1170	Aluminium composite panel	5	03-Sep-26	09-Sep-26	14-Sep-26 A	08-Oct-26
HAL-C-A-A-1250	Steel railing works	4	30-Aug-26	03-Sep-26	04-Oct-26	08-Oct-26
HAL-C-A-A-1160	Galvanised Steel Gratings	2	09-Sep-26	12-Sep-26	08-Oct-26	11-Oct-26
SPECIALTIES		3	20-Sep-26	24-Sep-26	08-Oct-26	12-Oct-26
HAL-C-A-A-1410	Identification sign; ID01 & ID02	3	20-Sep-26	24-Sep-26	08-Oct-26	12-Oct-26
MECHANICAL		32	27-Aug-26	19-Sep-26	16-Sep-26 A	10-Oct-26
HVAC		4	14-Sep-26	19-Sep-26	16-Sep-26 A	05-Oct-26
SECOND STAGE		4	14-Sep-26	19-Sep-26	16-Sep-26 A	05-Oct-26
HAL-C-A-M-770	Installation of Diffuser	2	14-Sep-26	16-Sep-26	16-Sep-26 A	04-Oct-26
HAL-C-A-M-960	Supply, install, test and commission door grilles & exhaust louv	2	16-Sep-26	19-Sep-26	16-Sep-26 A	05-Oct-26
SEWER AND DRAINAGE SYSTEM		10	27-Aug-26	08-Sep-26	28-Sep-26	10-Oct-26
SECOND STAGE		10	27-Aug-26	08-Sep-26	28-Sep-26	10-Oct-26
HAL-C-A-M-810	Installation of Sanitary Fixture and Accessories	4	27-Aug-26	01-Sep-26	28-Sep-26	03-Oct-26
HAL-C-A-M-830	Installation of Lavotary /Wash Basin	2	01-Sep-26	03-Sep-26	03-Oct-26	05-Oct-26
HAL-C-A-M-890	Installation of Bib Tap	2	03-Sep-26	06-Sep-26	05-Oct-26	07-Oct-26
HAL-C-A-M-850	Installation of Water Tap	2	06-Sep-26	08-Sep-26	07-Oct-26	10-Oct-26
ELECTRICAL		111	02-Sep-26	18-Nov-26	17-Jun-26 A	10-Oct-26
FIRST STAGE		75	11-Oct-26	15-Oct-26	17-Jun-26 A	05-Oct-26
HAL-C-A-E-573	Installation of Earthing and Grounding	4	11-Oct-26	15-Oct-26	17-Jun-26 A	05-Oct-26
HAL-C-A-E-683	Installation of LV Cables	2	11-Oct-26	15-Oct-26	22-Sep-26 A	05-Oct-26
SECOND STAGE		68	02-Sep-26	18-Nov-26	22-Aug-26 A	10-Oct-26
HAL-C-A-E-1030	Installation of CCTV System	2	08-Oct-26	17-Oct-26	22-Aug-26 A	06-Oct-26
HAL-C-A-E-1040	Installation of Solar power plant	2	10-Nov-26	18-Nov-26	22-Aug-26 A	29-Sep-26
HAL-C-A-E-733	Installation of Access Control System	2	24-Sep-26	30-Sep-26	22-Aug-26 A	07-Oct-26
HAL-C-A-E-703	Installation of LP-1 Panel	2	06-Oct-26	08-Oct-26	10-Sep-26 A	05-Oct-26
HAL-C-A-E-613	Installation of Lighting fixtures	2	04-Oct-26	08-Oct-26	22-Sep-26 A	06-Oct-26
HAL-C-A-E-583	Installation of Fire Alarm Control Panel	4	14-Sep-26	19-Sep-26	24-Sep-26 A	07-Oct-26
HAL-C-A-E-633	Installation of Wiring Devices	4	02-Sep-26	07-Sep-26	24-Sep-26 A	05-Oct-26
HAL-C-A-E-663	Installation of Disconnect Switches	2	07-Sep-26	09-Sep-26	24-Sep-26 A	06-Oct-26
HAL-C-A-E-743	Monitor Modules for Fire Alarm	2	30-Sep-26	03-Oct-26	24-Sep-26 A	06-Oct-26
HAL-C-A-E-753	Line Isolator Modules for Fire Alarm	2	03-Oct-26	05-Oct-26	24-Sep-26 A	06-Oct-26
HAL-C-A-E-593	Installation of Fire Detectors & Accessories	4	19-Sep-26	24-Sep-26	05-Oct-26	10-Oct-26
HAL-C-A-E-653	Installation of Main Distribution Board	2	04-Oct-26	06-Oct-26	05-Oct-26	07-Oct-26
HAL-C-A-E-673	Installation of Telephone Cabinet	2	11-Oct-26	13-Oct-26	05-Oct-26	07-Oct-26
HAL-C-A-E-713	Installation of PP-AC panel	2	08-Oct-26	11-Oct-26	05-Oct-26	07-Oct-26
BLOCK D		61	06-Sep-26	26-Nov-26	16-Apr-26 A	24-Oct-26
ARCHITECTURAL		10	06-Sep-26	15-Oct-26	27-Jul-26 A	24-Oct-26
WALL FINISHES		7	06-Sep-26	14-Sep-26	27-Jul-26 A	17-Oct-26
HAL-C-D-A-1090	Paint to Plaster (Primer, Putty & First Coat)	7	06-Sep-26	14-Sep-26	27-Jul-26 A	17-Oct-26
FLOOR FINISHES		2	07-Oct-26	15-Oct-26	03-Sep-26 A	24-Oct-26
HAL-C-D-A-1260	Epoxy paint	2	07-Oct-26	15-Oct-26	03-Sep-26 A	24-Oct-26
METAL WORKS		5	15-Sep-26	21-Sep-26	02-Aug-26 A	21-Oct-26
HAL-C-D-A-1170	Aluminium composite panel	5	15-Sep-26	21-Sep-26	02-Aug-26 A	21-Oct-26
ELECTRICAL		57	14-Sep-26	26-Nov-26	16-Apr-26 A	19-Oct-26
FIRST STAGE		44	15-Oct-26	20-Oct-26	16-Apr-26 A	18-Oct-26
HAL-C-D-E-573	Installation of Earthing and Grounding	4	15-Oct-26	20-Oct-26	16-Apr-26 A	18-Oct-26
HAL-C-D-E-683	Installation of LV Cables	4	15-Oct-26	20-Oct-26	05-Sep-26 A	18-Oct-26
SECOND STAGE		57	14-Sep-26	26-Nov-26	17-Jun-26 A	19-Oct-26
HAL-C-D-E-1030	Installation of CCTV System	2	18-Oct-26	26-Oct-26	17-Jun-26 A	18-Oct-26
HAL-C-D-E-733	Installation of Access Control System	2	06-Oct-26	12-Oct-26	17-Jun-26 A	19-Oct-26
HAL-C-D-E-673	Installation of Telephone Cabinet	2	20-Oct-26	22-Oct-26	29-Jul-26 A	18-Oct-26

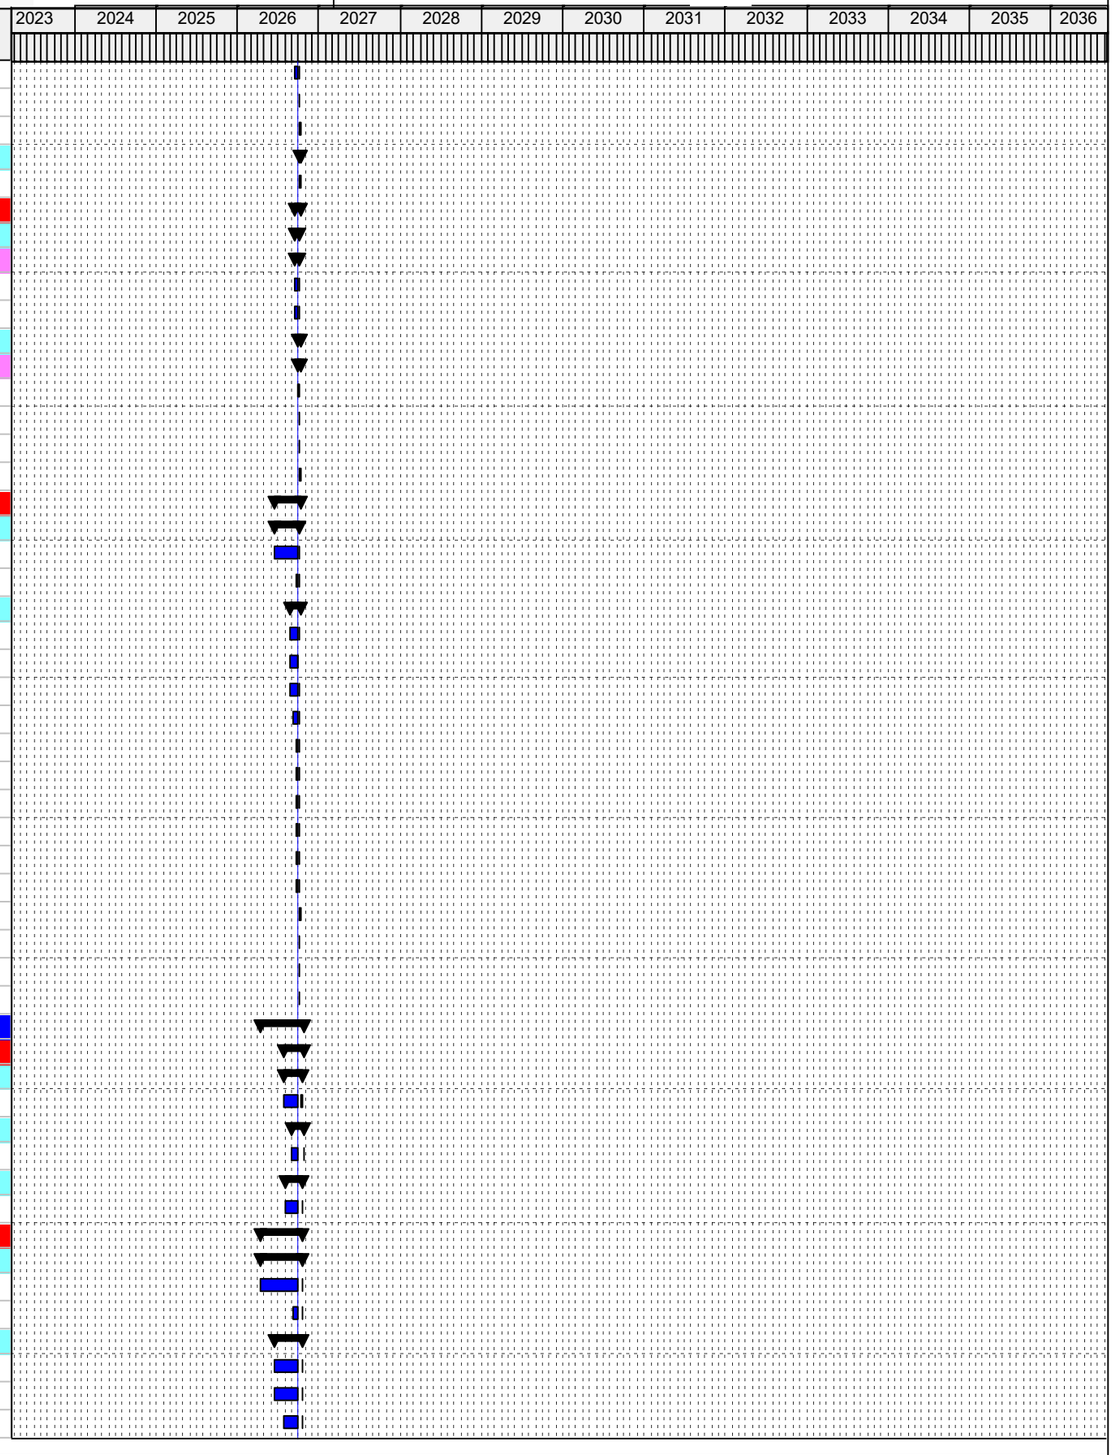

Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary

Date	Revision	Checked	Approved
28-Sep-26	Weekly Report#038		


Activity ID	Activity Name	Original Duration	BL Project Start	BL Project Finish	Start	Finish
HAL-C-D-E-1040	Installation of Solar power plant	2	18-Nov-26	26-Nov-26	15-Aug-26 A	18-Oct-26
HAL-C-D-E-633	Installation of Wiring Devices	4	14-Sep-26	19-Sep-26	29-Aug-26 A	17-Oct-26
HAL-C-D-E-663	Installation of Disconnect Switches	2	19-Sep-26	21-Sep-26	29-Aug-26 A	17-Oct-26
HAL-C-D-E-713	Installation of PP-AC panel	2	18-Oct-26	20-Oct-26	02-Sep-26 A	18-Oct-26
HAL-C-D-E-653	Installation of Main Distribution Board	2	15-Oct-26	18-Oct-26	03-Sep-26 A	18-Oct-26
HAL-C-D-E-613	Installation of Lighting fixtures	4	15-Oct-26	20-Oct-26	08-Sep-26 A	18-Oct-26
HAL-C-D-E-593	Installation of Fire Detectors & Accessories	4	01-Oct-26	06-Oct-26	22-Sep-26 A	18-Oct-26
HAL-C-D-E-743	Monitor Modules for Fire Alarm	2	12-Oct-26	14-Oct-26	24-Sep-26 A	19-Oct-26
HAL-C-D-E-753	Line Isolator Modules for Fire Alarm	2	14-Oct-26	17-Oct-26	24-Sep-26 A	19-Oct-26
BLOCK E		43	26-Jul-26	26-Nov-26	05-Apr-26 A	01-Nov-26
ARCHITECTURAL		13	02-Sep-26	08-Oct-26	12-Aug-26 A	01-Nov-26
WALL FINISHES		7	02-Sep-26	10-Sep-26	12-Aug-26 A	01-Nov-26
HAL-C-E-A-230	Paint to Plaster (Primer, Putty & First Coat)	7	02-Sep-26	10-Sep-26	12-Aug-26 A	01-Nov-26
FLOOR FINISHES		5	30-Sep-26	08-Oct-26	05-Sep-26 A	21-Oct-26
HAL-C-E-A-420	Epoxy paint	5	30-Sep-26	08-Oct-26	05-Sep-26 A	21-Oct-26
METAL WORKS		5	12-Sep-26	17-Sep-26	13-Aug-26 A	18-Oct-26
HAL-C-E-A-292	Aluminium composite panel	5	12-Sep-26	17-Sep-26	13-Aug-26 A	18-Oct-26
ELECTRICAL		43	26-Jul-26	26-Nov-26	05-Apr-26 A	01-Nov-26
FIRST STAGE		29	18-Aug-26	29-Aug-26	05-Apr-26 A	19-Oct-26
HAL-C-E-E-113	Installation of Earthing and Grounding	5	23-Aug-26	29-Aug-26	05-Apr-26 A	19-Oct-26
HAL-C-E-E-223	Installation of LV Cables	4	18-Aug-26	23-Aug-26	05-Sep-26 A	18-Oct-26
SECOND STAGE		43	26-Jul-26	26-Nov-26	17-Jun-26 A	01-Nov-26
HAL-C-E-E-410	Installation of CCTV System	7	09-Aug-26	17-Aug-26	17-Jun-26 A	19-Oct-26
HAL-C-E-E-273	Installation of Access Control System	5	17-Aug-26	23-Aug-26	17-Jun-26 A	24-Oct-26
HAL-C-E-E-243	Installation of LP-1 Panel	2	11-Aug-26	13-Aug-26	26-Jul-26 A	17-Oct-26
HAL-C-E-E-213	Installation of Telephone Cabinet	2	16-Aug-26	18-Aug-26	30-Jul-26 A	17-Oct-26
HAL-C-E-E-420	Installation of Solar power plant	2	18-Nov-26	26-Nov-26	17-Aug-26 A	18-Oct-26
HAL-C-E-E-173	Installation of Wiring Devices	4	10-Sep-26	15-Sep-26	29-Aug-26 A	01-Nov-26
HAL-C-E-E-193	Installation of Main Distribution Board	2	09-Aug-26	11-Aug-26	08-Sep-26 A	15-Oct-26
HAL-C-E-E-153	Installation of Lighting fixtures	4	09-Aug-26	13-Aug-26	15-Sep-26 A	15-Oct-26
HAL-C-E-E-253	Installation of PP-AC panel	2	13-Aug-26	16-Aug-26	17-Sep-26 A	17-Oct-26
HAL-C-E-E-133	Installation of Fire Detectors & Accessories	4	26-Jul-26	30-Jul-26	22-Sep-26 A	15-Oct-26
HAL-C-E-E-283	Monitor Modules for Fire Alarm	2	23-Aug-26	25-Aug-26	24-Sep-26 A	25-Oct-26
HAL-C-E-E-293	Line Isolator Modules for Fire Alarm	2	25-Aug-26	27-Aug-26	24-Sep-26 A	27-Oct-26
SITE INFRASTRUCTURE		45	05-Aug-26	14-Nov-26	25-Jul-26 A	11-Nov-26
EXTERNAL WORKS		45	05-Aug-26	14-Nov-26	25-Jul-26 A	11-Nov-26
MECHANICAL		1	31-Oct-26	01-Nov-26	10-Oct-26	10-Oct-26
HAL-C-EX-M-1311	CO2 fire extinguisher	1	31-Oct-26	01-Nov-26	10-Oct-26	10-Oct-26
ELECTRICAL		35	27-Sep-26	14-Nov-26	25-Jul-26 A	20-Oct-26
HAL-C-EX-E-186	Installation of Earthing and Grounding	5	29-Sep-26	05-Oct-26	25-Jul-26 A	14-Oct-26
HAL-C-EX-E-206	Installation of Conduites for Lighting Fixture	4	05-Oct-26	10-Oct-26	19-Aug-26 A	17-Oct-26
HAL-C-EX-E-1341	Installation of Cable tray	2	02-Nov-26	08-Nov-26	05-Sep-26 A	11-Oct-26
HAL-C-EX-E-1321	Installation of wiring devices	2	02-Nov-26	08-Nov-26	24-Sep-26 A	12-Oct-26
HAL-C-EX-E-176	Installation of Main MCC	2	27-Sep-26	29-Sep-26	24-Sep-26 A	11-Oct-26
HAL-C-EX-E-196	Installation of Lighting fixtures	2	12-Oct-26	14-Oct-26	24-Sep-26 A	20-Oct-26
HAL-C-EX-E-216	Installation of LV Cables	2	08-Nov-26	14-Nov-26	24-Sep-26 A	11-Oct-26
HAL-C-EX-E-236	Installation of panel boards	2	31-Oct-26	02-Nov-26	24-Sep-26 A	11-Oct-26
EXTERNAL ELECTRICAL WORKS		18	05-Aug-26	16-Sep-26	10-Sep-26 A	11-Nov-26
HAL-C-EX-E-470	Installation of Earthing and Grounding	5	05-Sep-26	10-Sep-26	10-Sep-26 A	05-Nov-26
HAL-C-EX-E-480	Installation of Street Lighting Feeder pillars & KWH meter	5	10-Sep-26	16-Sep-26	10-Sep-26 A	11-Nov-26

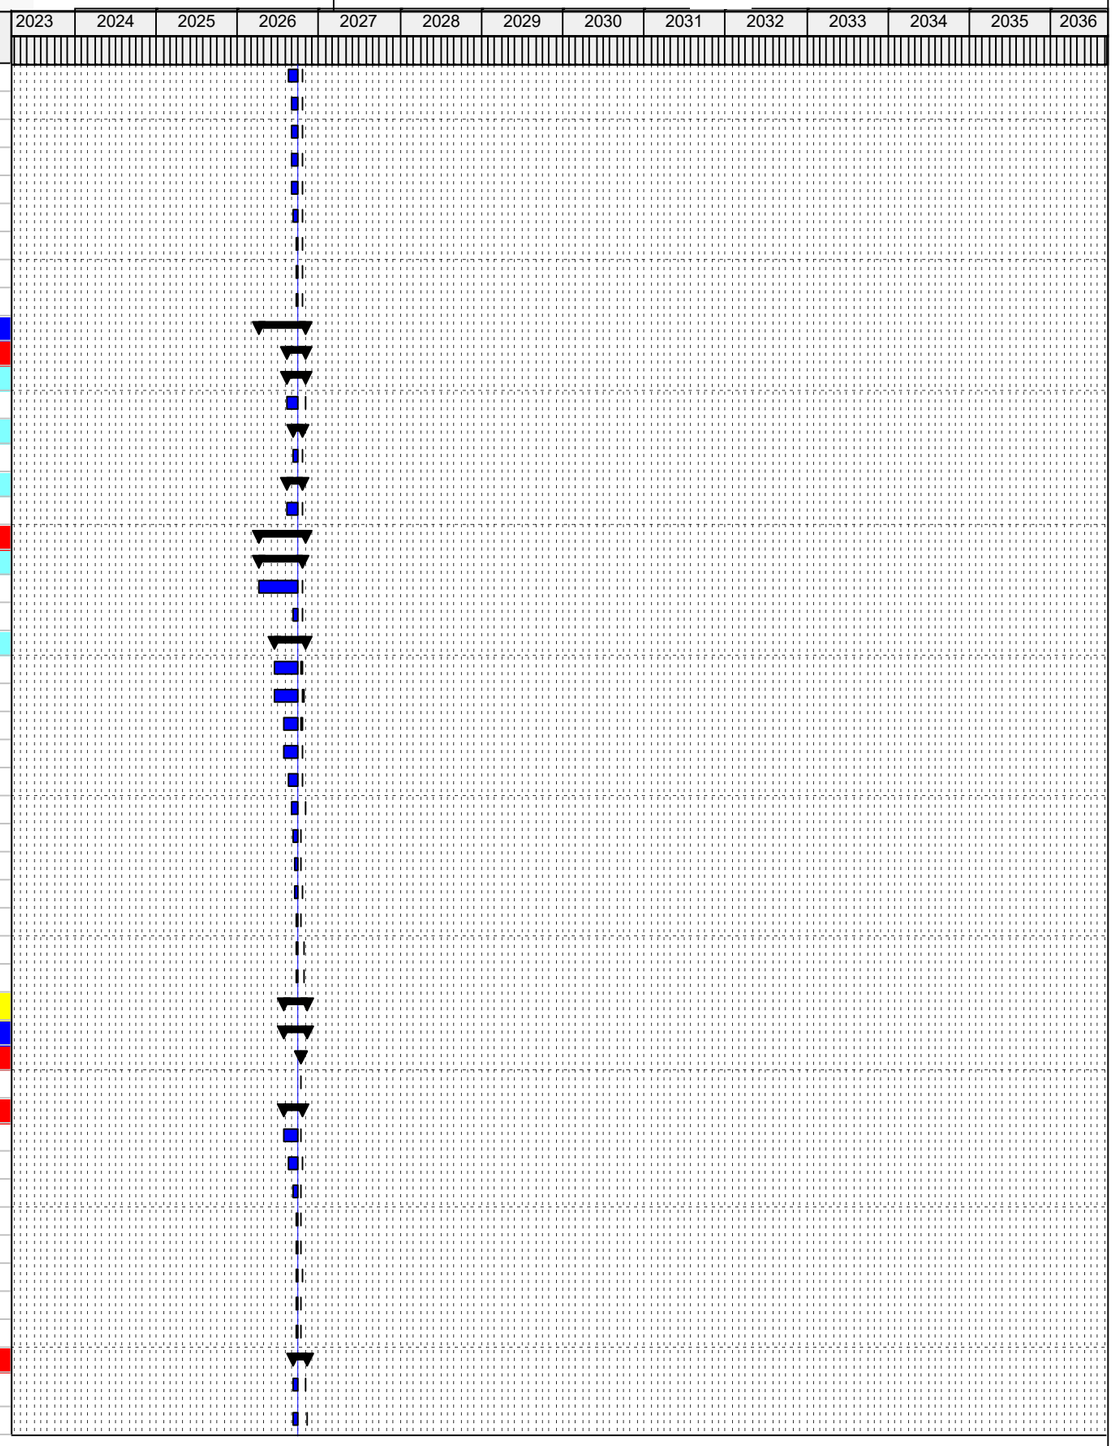

Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary

Date	Revision	Checked	Approved
28-Sep-26	Weekly Report#038		

Activity ID	Activity Name	Original Duration	BL Project Start	BL Project Finish	Start	Finish
HAL-C-EX-E-440	Installation of Lighting poles	7	05-Aug-26	13-Aug-26	24-Sep-26 A	14-Oct-26
ROAD WORKS		21	12-Sep-26	26-Oct-26	19-Sep-26 A	21-Oct-26
HAL-C-EX-R-1460	Curb Stones	7	12-Sep-26	29-Sep-26	19-Sep-26 A	10-Oct-26
HAL-C-EX-R-1480	Interlock Tiles	7	29-Sep-26	15-Oct-26	24-Sep-26 A	12-Oct-26
HAL-C-EX-R-1500	Road Signs	5	20-Oct-26	26-Oct-26	24-Sep-26 A	21-Oct-26
TESTING AND COMMISSIONING (10%)		33	18-Aug-26	29-Nov-26	08-Sep-26 A	04-Nov-26
TESTING AND COMMISSIONING 900 Sq.m-2		21	08-Sep-26	29-Nov-26	08-Sep-26 A	04-Nov-26
MECHANICAL		21	08-Sep-26	11-Oct-26	08-Sep-26 A	04-Nov-26
HAL-C-TC-M-3376	Testing and Commissioning of Fire Fighting Pipes	7	22-Sep-26	01-Oct-26	08-Sep-26 A	01-Nov-26
HAL-C-TC-M-3416	Testing and Commissioning of Electric Water Heater	7	08-Sep-26	16-Sep-26	15-Sep-26 A	21-Oct-26
HAL-C-TC-M3446	Testing and Commissioning of Exhaust Fan	7	16-Sep-26	26-Sep-26	15-Sep-26 A	04-Nov-26
HAL-C-TC-M-3456	Testing and Commissioning of Wall propeller type exhaust fan	7	21-Sep-26	30-Sep-26	15-Sep-26 A	04-Nov-26
HAL-C-TC-M-3386	Testing and Commissioning of Fire Hose Cabinet	3	03-Oct-26	11-Oct-26	24-Sep-26 A	01-Nov-26
HAL-C-TC-M-3426	Testing and Commissioning of Sanitary Fixtures	7	16-Sep-26	26-Sep-26	24-Sep-26 A	21-Oct-26
ELECTRICAL		1	26-Nov-26	29-Nov-26	15-Sep-26 A	18-Oct-26
HAL-C-TC-E-3556	Testing and Commissioning of Solar power plant	1	26-Nov-26	29-Nov-26	15-Sep-26 A	18-Oct-26
TESTING AND COMMISSIONING SITE INFRASTRUCTURE		25	18-Aug-26	14-Nov-26	15-Sep-26 A	26-Oct-26
PUMP ROOM SHED		20	27-Sep-26	14-Nov-26	15-Sep-26 A	26-Oct-26
HAL-C-TC-M-3576	Testing & Commissioning of Fire Fighting pump	2	31-Oct-26	05-Nov-26	15-Sep-26 A	26-Oct-26
HAL-C-TC-M-3586	Testing & Commissioning of Booster pump	2	27-Sep-26	05-Oct-26	15-Sep-26 A	26-Oct-26
HAL-C-TC-E-3621	Testing and Commissioning of LV cables	2	08-Nov-26	14-Nov-26	10-Oct-26	11-Oct-26
ENVIRONMENTAL		5	18-Aug-26	28-Oct-26	15-Sep-26 A	10-Oct-26
HAL-C-TC-E-3666	Testing and Commissioning of Main program system & contro	5	11-Oct-26	28-Oct-26	15-Sep-26 A	10-Oct-26
HAL-C-TC-ENV-SW-7	Testing & Commissioning of Irrigaiton System	5	18-Aug-26	24-Aug-26	15-Sep-26 A	10-Oct-26

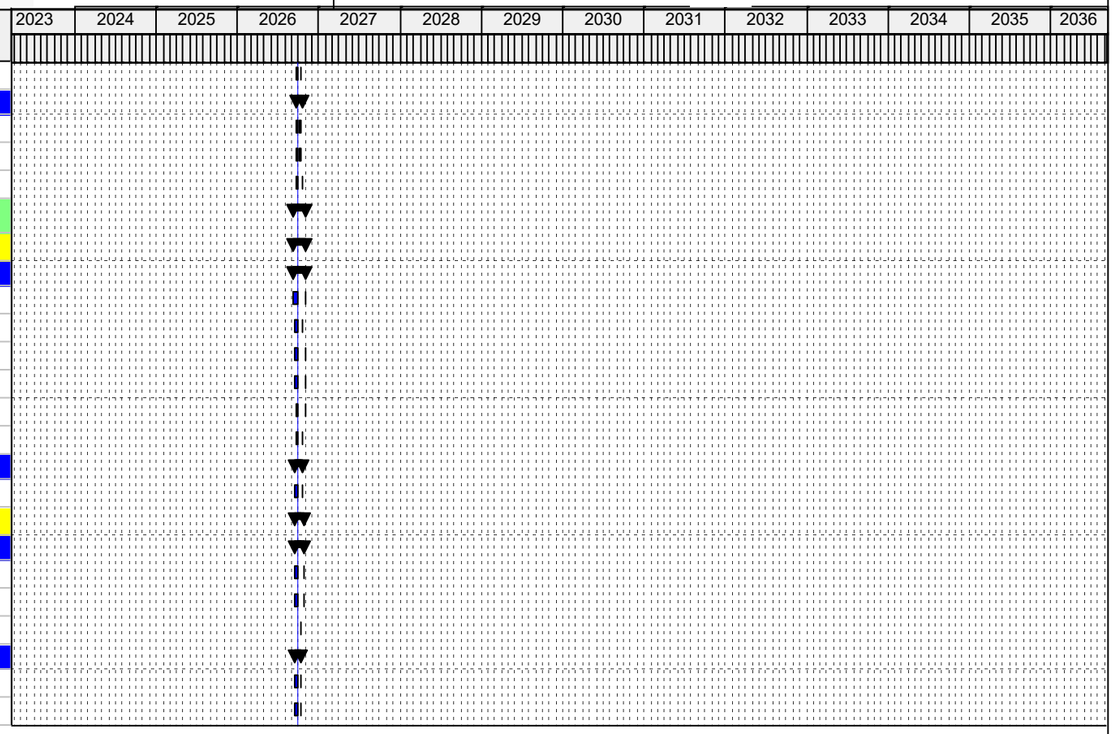

Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary

Date	Revision	Checked	Approved
28-Sep-26	Weekly Report#038		
