
MLTX-02-004 - Playground Initiative for Western Region (Asir-Jazan -Jeddah)

Updateded schedule D.D 26-10-2026

ActivityID	ActivityName	Orginal Duration	Schedule %	Performance% Complete	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Variance - BL Project
MLTX-02-004 - Playground Initiative for Western Region (Asir - Jazan - Je		34900	4335%	3763%	26-Mar-26	25Jan-27	26-Mar-26A	19May-27	$14647,967.63	$12715,611.94	$33793,600.34	-9100
KEY MILESTONES		34900	0%	0%	26-Mar-26	25Jan-27	26-Mar-26A	19May-27	$000	$000	$0.00	-9100
GENERAL MILESTONES		34900	0%	0%	26-Mar-26	25Jan-27	26-Mar-26A	19May-27	$000	$000	$0.00	-9100
MLTX-02-004MS-1030	Project Completion	0.00	0%	0%		25Jan-27		19May-27	$000	$000	$0.00	0.00
MLTX-02-004MS-1010	Project CommencementDate	0.00	100%	100%	26-Mar-26		26-Mar-26A		$000	$000	$0.00	0.00
CONTRACTUAL MILESTONE		31900	0%	0%	29-Apr-26	25Jan-27	29-Apr-26A	19May-27	$000	$000	$0.00	-9100
MLTX-02-004MS-1160	Completionof Asir Works	0.00	0%	0%		19Jan-27		05Apr-27	$000	$000	$0.00	0.00
MLTX-02-004MS-1170	Completionof Jazan Works	0.00	0%	0%		25Jan-27		19May-27	$000	$000	$0.00	0.00
MLTX-02-004MS-1180	Completionof Jeddah Works	0.00	0%	0%		25Jan-27		01Apr-27	$000	$000	$0.00	0.00
MLTX-02-004MS-1100	Completionof Engineering	0.00	100%	0%		22Jul-26		12Nov-26	$000	$000	$0.00	0.00
MLTX-02-004MS-1120	Completionof Levelling Works	0.00	100%	0%		09Aug-26		27Oct-26	$000	$000	$0.00	0.00
MLTX-02-004MS-1070	Completionof Testing& Commissioning	0.00	0%	0%		19Jan-27		18Apr-27	$000	$000	$0.00	0.00
MLTX-02-004MS-1130	Completionof ToiletBuilding	0.00	0%	0%		30Nov-26		11Jan-27	$000	$000	$0.00	0.00
MLTX-02-004MS-1140	Completionof Playground Area	0.00	0%	0%		16Jan-27		06May-27	$000	$000	$0.00	0.00
MLTX-02-004MS-1150	Completionof NaturalLandscape Works	0.00	0%	0%		13Dec-26		18Mar-27	$000	$000	$0.00	0.00
MLTX-02-004MS-1050	Completionof Mobilization	0.00	100%	100%		02Jun-26		02Jun-26A	$000	$000	$0.00	0.00
MLTX-02-004MS-1060	Baseline ProgrammeApproval	0.00	100%	100%		29Apr-26		29Apr-26A	$000	$000	$0.00	0.00
JEDDAH		31100	5436%	4336%	26-Mar-26	25Jan-27	26-Mar-26A	01Apr-27	$6814,482.06	$5435,065.36	$12535,459.74	-5300
MOBILIZATION		6300	0%	0%	26-Mar-26	10Jun-26	26-Mar-26A	10Jun-26A	$000	$000	$0.00	0.00
TOPOGRAPHICSURVEY		4.00	0%	0%	26-Mar-26	30Mar-26	26-Mar-26A	30Mar-26A	$000	$000	$0.00	0.00
MLTX-02-004MB-2100	Site Survey Works	4.00	100%	100%	26-Mar-26	30Mar-26	26-Mar-26A	30Mar-26A	$000	$000	$0.00	0.00
SITEFACILITIES & OFFICES		5575	0%	0%	26-Mar-26	02Jun-26	26-Mar-26A	02Jun-26A	$000	$000	$0.00	0.00
MLTX-02-004MB-1980	Manpower Mobalizaton	31.50	100%	100%	16-Apr-26	23May-26	16-Apr-26A	23May-26A	$000	$000	$0.00	0.00
MLTX-02-004MB-1990	Equipment Mobalization	1.40	100%	100%	14-Apr-26	15Apr-26	14-Apr-26A	15Apr-26A	$000	$000	$0.00	0.00
MLTX-02-004MB-2010	Site Layout Plan	4.00	100%	100%	26-Mar-26	30Mar-26	26-Mar-26A	30Mar-26A	$000	$000	$0.00	0.00
MLTX-02-004MB-2020	Clear & Grub forOffices & AccessRoad	5.00	100%	100%	07-Apr-26	12Apr-26	07-Apr-26A	12Apr-26A	$000	$000	$0.00	0.00
MLTX-02-004MB-2030	ConstuctSiteAccess Roads	2.00	100%	100%	11-Apr-26	12Apr-26	10-Apr-26A	12Apr-26A	$000	$000	$0.00	0.00
MLTX-02-004MB-2040	ConstuctTemporay Fence	3975	100%	100%	14-Apr-26	02Jun-26	14-Apr-26A	02Jun-26A	$000	$000	$0.00	0.00
MLTX-02-004MB-2050	ConstuctSiteOffices & Storage	2333	100%	100%	15-Apr-26	12May-26	15-Apr-26A	12May-26A	$000	$000	$0.00	0.00
MLTX-02-004MB-2060	InstallProject Signs	4.60	100%	100%	26-Apr-26	30Apr-26	26-Apr-26A	30Apr-26A	$000	$000	$0.00	0.00
MLTX-02-004MB-2070	InstallSiteFacilities	2872	100%	100%	08-Apr-26	11May-26	08-Apr-26A	11May-26A	$000	$000	$0.00	0.00
MLTX-02-004MB-2080	Electrical Works & Connections	2340	100%	100%	15-Apr-26	12May-26	15-Apr-26A	12May-26A	$000	$000	$0.00	0.00
MLTX-02-004MB-2090	ConstuctParking Sheds	6.00	100%	100%	12-Apr-26	18Apr-26	12-Apr-26A	18Apr-26A	$000	$000	$0.00	0.00
PRELIMNARY SUBMITTALS		5900	0%	0%	31-Mar-26	10Jun-26	31-Mar-26A	10Jun-26A	$000	$000	$0.00	0.00
PREPARATIONS& SUBMITTAL BY CONTRACTORS		2700	0%	0%	31-Mar-26	30Apr-26	31-Mar-26A	30Apr-26A	$000	$000	$0.00	0.00
MLTX-02-004MB-2000	Preparation andSubmittal ofDetaledWorkOrderProgramme(Baseline)	2500	100%	100%	31-Mar-26	28Apr-26	31-Mar-26A	28Apr-26A	$000	$000	$0.00	0.00
MLTX-02-004MB-2110	Preparation andSubmittal ofProject Execution Plan	2700	100%	100%	31-Mar-26	30Apr-26	31-Mar-26A	30Apr-26A	$000	$000	$0.00	0.00
MLTX-02-004MB-2120	Submissionof Contactor Project Quality Plan	1000	100%	100%	31-Mar-26	11Apr-26	31-Mar-26A	11Apr-26A	$000	$000	$0.00	0.00
MLTX-02-004MB-2130	Submissionof Construction Safety& EnvironmentalManagement Plan	1000	100%	100%	31-Mar-26	11Apr-26	31-Mar-26A	11Apr-26A	$000	$000	$0.00	0.00
MLTX-02-004MB-2140	Preparation andSubmittal ofOrganizaton Chat	8.00	100%	100%	31-Mar-26	08Apr-26	31-Mar-26A	08Apr-26A	$000	$000	$0.00	0.00
MLTX-02-004MB-2150	Preparation andSubmittal ofCommunication Plan	8.00	100%	100%	31-Mar-26	08Apr-26	31-Mar-26A	08Apr-26A	$000	$000	$0.00	0.00
APPROVALS BYEMPLOYERS		5100	0%	0%	09-Apr-26	10Jun-26	09-Apr-26A	10Jun-26A	$000	$000	$0.00	0.00
MLTX-02-004MB-2160	Appoval of DetaledWorkOrderProgramme (Baseline)	1.00	100%	100%	29-Apr-26	29Apr-26	29-Apr-26A	29Apr-26A	$000	$000	$0.00	0.00
MLTX-02-004MB-2170	Appoval of Project Execution Plan	1.00	100%	100%	13-May-26	13May-26	13 May 26 A	13May-26A	$000	$000	$0.00	0.00
MLTX-02-004MB-2180	Appoval of ContactorProject QualityPlan	1900	100%	100%	09-Apr-26	30Apr-26	09-Apr-26A	30Apr-26A	$000	$000	$0.00	0.00
MLTX-02-004MB-2190	Appoval of Constuction Safety & EnvironmentalManagement Plan	1.00	100%	100%	10-Jun-26	10Jun-26	10 Jun 26 A	10Jun-26A	$000	$000	$0.00	0.00
MLTX-02-004MB-2200	Appoval of Organization Chat	1000	100%	100%	09-Apr-26	20Apr-26	09-Apr-26A	20Apr-26A	$000	$000	$0.00	0.00
MLTX-02-004MB-2210	Appoval of Communication Plan	1000	100%	100%	09-Apr-26	20Apr-26	09-Apr-26A	20Apr-26A	$000	$000	$0.00	0.00
ENGINEERING		19100	0%	0%	31-Mar-26	21Jul-26	31-Mar-26A	12Nov-26	$000	$000	$0.00	-9700
SHOP DRAWINGS		14400	0%	0%	31-Mar-26	21Jul-26	31-Mar-26A	26Aug-26A	$000	$000	$0.00	-3100
SHOP DRAWINGS SUBMISSION		13600	0%	0%	31-Mar-26	12Jul-26	31-Mar-26A	25Aug-26A	$000	$000	$0.00	-3800
SHOP DRAWINGSUBMITTALS FOR EARTHINGWORKS		5800	0%	0%	31-Mar-26	09Jun-26	31-Mar-26A	09Jun-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-12100	ShopDWG SubmittalforLayoutPlan	2000	100%	100%	31-Mar-26	22Apr-26	31-Mar-26A	22Apr-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-12110	ShopDWG SubmittalforSetting Out	2200	100%	100%	31-Mar-26	25Apr-26	31-Mar-26A	25Apr-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-12120	ShopDWG SubmittalforGrading Layat Plan	2300	100%	100%	31-Mar-26	26Apr-26	31-Mar-26A	26Apr-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-12130	ShopDWG SubmittalforCurb Setting OutPoints	1.00	100%	100%	21-May-26	21May-26	21 May 26 A	21May-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-12140	ShopDWG SubmittalforSigning & MakingLayoutPlan	1.00	100%	100%	09-Jun-26	09Jun-26	09 Jun 26 A	09Jun-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-12150	ShopDWG SubmittalforStandards Details	1.00	100%	100%	21-May-26	21May-26	21 May 26 A	21May-26A	$000	$000	$0.00	0.00
SHOP DRAWINGSUBMITTALS FOR SERVCE/TOILETWORKS		13600	0%	0%	31-Mar-26	12Jul-26	31-Mar-26A	25Aug-26A	$000	$000	$0.00	-3800
ARCHITECTURE WORKS		1200	0%	0%	31-Mar-26	13Apr-26	31-Mar-26A	13Apr-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-124	ShopDWG SubmittalforFloorPlan	1200	100%	100%	31-Mar-26	13Apr-26	31-Mar-26A	13Apr-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-124	ShopDWG SubmittalforElevatons	1200	100%	100%	31-Mar-26	13Apr-26	31-Mar-26A	13Apr-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-125	ShopDWG SubmittalforSections	1200	100%	100%	31-Mar-26	13Apr-26	31-Mar-26A	13Apr-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-125	ShopDWG SubmittalforCeiling Plan	1200	100%	100%	31-Mar-26	13Apr-26	31-Mar-26A	13Apr-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-125	ShopDWG SubmittalforFinishes Plan	1200	100%	100%	31-Mar-26	13Apr-26	31-Mar-26A	13Apr-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-125	ShopDWG SubmittalforToilet Details	1200	100%	100%	31-Mar-26	13Apr-26	31-Mar-26A	13Apr-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-125	ShopDWG SubmittalforDoors&Windows Schedule	1200	100%	100%	31-Mar-26	13Apr-26	31-Mar-26A	13Apr-26A	$000	$000	$0.00	0.00
STRUCTUREWORKS		9.00	0%	0%	08-Apr-26	18Apr-26	08-Apr-26A	18Apr-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-125	ShopDWG SubmittalforFoundationPlan	9.00	100%	100%	08-Apr-26	18Apr-26	08-Apr-26A	18Apr-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-125	ShopDWG SubmittalforGroundFloorFraming Plan	9.00	100%	100%	08-Apr-26	18Apr-26	08-Apr-26A	18Apr-26A	$000	$000	$0.00	0.00

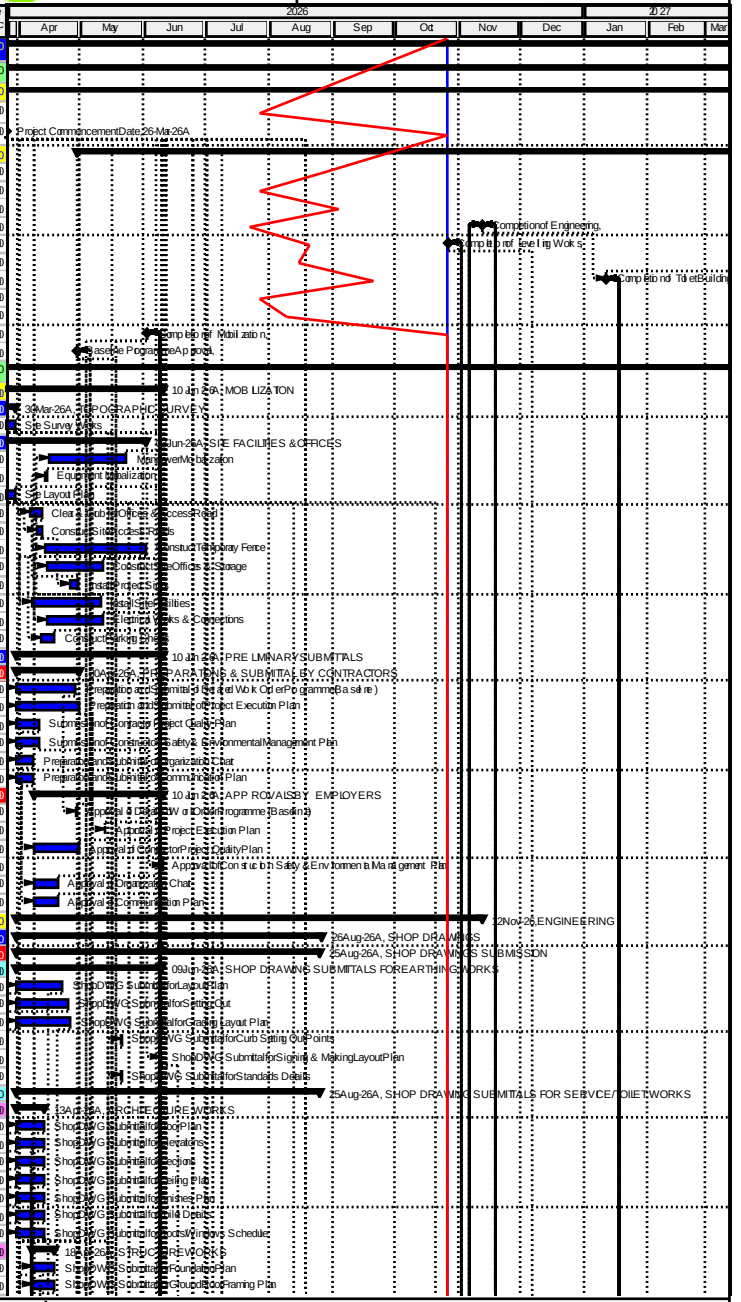


Actual Level of Effort | Remaining Work | Actual Work | Critical Remaining Work

TASK filter: All Activities


© Oracle Corporation

ActivityID	ActivityName	Orginal Duration	Schedule %	Performance% Complete	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Variance - BL Project
MLTX02-004EN-12(	ShopDWG SubmittalforSections/Details	9.0	100%	100%	08 Apr 26	18Apr-26	08 Apr26 A	18Apr-26A	$000	$000	$0.00	0.0
MECHANCAL WORKS		3800	0%	0%	08 Apr 26	21May-26	08 Apr26 A	21May-26A	$000	$000	$0.00	0.0
MLTX02-004EN-12(	ShopDWG SubmittalforHVAC Plan	6.0	100%	100%	08 Apr 26	14Apr-26	08 Apr26 A	14Apr-26A	$000	$000	$0.00	0.0
MLTX02-004EN-12(	ShopDWG SubmittalforExhaustAirPlan	6.0	100%	100%	08 Apr 26	14Apr-26	08 Apr26 A	14Apr-26A	$000	$000	$0.00	0.0
MLTX02-004EN-12(	ShopDWG SubmittalforHVAC Equipment Schedule	6.0	100%	100%	08 Apr 26	14Apr-26	08 Apr26 A	14Apr-26A	$000	$000	$0.00	0.0
MLTX02-004EN-12(	ShopDWG SubmittalforFireFighting Layout	6.0	100%	100%	08 Apr 26	14Apr-26	08 Apr26 A	14Apr-26A	$000	$000	$0.00	0.0
MLTX02-004EN-12(	ShopDWG SubmittalforWaterSupply Layout	1.0	100%	100%	06 May-26	06May-26	06 May 26 A	06May-26A	$000	$000	$0.00	0.0
MLTX02-004EN-12(	ShopDWG SubmittalforWaterSupply Details	6.0	100%	100%	08 Apr 26	14Apr-26	08 Apr26 A	14Apr-26A	$000	$000	$0.00	0.0
MLTX02-004EN-12(	ShopDWG SubmittalforDrainage Layout	6.0	100%	100%	08 Apr 26	14Apr-26	08 Apr26 A	14Apr-26A	$000	$000	$0.00	0.0
MLTX02-004EN-12(	ShopDWG SubmittalforDrainage Details	1.0	100%	100%	21 May-26	21May-26	21 May 26 A	21May-26A	$000	$000	$0.00	0.0
MLTX02-004EN-13(	ShopDWG SubmittalforDut RoutingLayout	1.0	100%	100%	06 May-26	06May-26	06 May 26 A	06May-26A	$000	$000	$0.00	0.0
MLTX02-004EN-13(	ShopDWG SubmittalforDiffusersLayout	1.0	100%	100%	21 May-26	21May-26	21 May 26 A	21May-26A	$000	$000	$0.00	0.0
ELECTRCAL WORKS		12900	0%	0%	08 Apr 26	12Jul-26	08 Apr26 A	25Aug-26A	$000	$000	$0.00	-3800
MLTX02-004EN-12(	ShopDWG SubmittalforLighting Layout	6.0	100%	100%	08 Apr 26	14Apr-26	08 Apr26 A	14Apr-26A	$000	$000	$0.00	0.0
MLTX02-004EN-12(	ShopDWG SubmittalforPower Layout	6.0	100%	100%	08 Apr 26	14Apr-26	08 Apr26 A	14Apr-26A	$000	$000	$0.00	0.0
MLTX02-004EN-12(	ShopDWG SubmittalforPower SingleLineDiagram	1.0	100%	100%	06 May-26	06May-26	06 May 26 A	06May-26A	$000	$000	$0.00	0.0
MLTX02-004EN-12(	ShopDWG SubmittalforPanelBoardSchedules	1.0	100%	100%	06 May-26	06May-26	06 May 26 A	06May-26A	$000	$000	$0.00	0.0
MLTX02-004EN-12(	ShopDWG SubmittalforLighting Instalation Details	6.0	100%	100%	08 Apr 26	14Apr-26	08 Apr26 A	14Apr-26A	$000	$000	$0.00	0.0
MLTX02-004EN-12(	ShopDWG SubmittalforPower Instalation Details	6.0	100%	100%	08 Apr 26	14Apr-26	08 Apr26 A	14Apr-26A	$000	$000	$0.00	0.0
MLTX02-004EN-12(	ShopDWG SubmittalforCableTrayInstalation Details	1.0	100%	100%	06 May-26	06May-26	06 May 26 A	06May-26A	$000	$000	$0.00	0.0
MLTX02-004EN-12(	ShopDWG SubmittalforManhole& Ductbank Details	1.0	100%	100%	06 May-26	06May-26	06 May 26 A	06May-26A	$000	$000	$0.00	0.0
MLTX02-004EN-12(	ShopDWG SubmittalforGrounding Details	1.0	100%	100%	06 May-26	06May-26	06 May 26 A	06May-26A	$000	$000	$0.00	0.0
MLTX02-004EN-12(	ShopDWG SubmittalforLightningProtection Details	6.0	100%	100%	08 Apr 26	14Apr-26	08 Apr26 A	14Apr-26A	$000	$000	$0.00	0.0
MLTX02-004EN-12(	ShopDWG SubmittalforFireAlarmInstallation Details	11.0	100%	100%	08 Apr 26	20Apr-26	08 Apr26 A	20Apr-26A	$000	$000	$0.00	0.0
MLTX02-004EN-12(	ShopDWG SubmittalforCCTV Details	3.0	100%	100%	09 Jul-26	12Jul-26	25 Aug 26 A	25Aug-26A	$000	$000	$0.00	2.0
MLTX02-004EN-12(	ShopDWG SubmittalforGrounding Layout	1.0	100%	100%	06 May-26	06May-26	06 May 26 A	06May-26A	$000	$000	$0.00	0.0
MLTX02-004EN-12(	ShopDWG SubmittalforLightningProtection System Layout	6.0	100%	100%	08 Apr 26	14Apr-26	08 Apr26 A	14Apr-26A	$000	$000	$0.00	0.0
MLTX02-004EN-12(	ShopDWG SubmittalforFireAlarmLayout	11.0	100%	100%	08 Apr 26	20Apr-26	08 Apr26 A	20Apr-26A	$000	$000	$0.00	0.0
MLTX02-004EN-12(	ShopDWG SubmittalforFireAlarmRiserDiagram	11.0	100%	100%	08 Apr 26	20Apr-26	08 Apr26 A	20Apr-26A	$000	$000	$0.00	0.0
MLTX02-004EN-12(	ShopDWG SubmittalforCCTV Layout	5.0	100%	100%	05 Jul-26	09Jul-26	25 Aug 26 A	25Aug-26A	$000	$000	$0.00	4.0
MLTX02-004EN-12(	ShopDWG SubmittalforCCTV Riser Diagram	5.0	100%	100%	05 Jul-26	09Jul-26	25 Aug 26 A	25Aug-26A	$000	$000	$0.00	4.0
MLTX02-004EN-12(	ShopDWG SubmittalforTelephone & Data Layout	11.0	100%	100%	08 Apr 26	20Apr-26	08 Apr26 A	20Apr-26A	$000	$000	$0.00	0.0
MLTX02-004EN-12(	ShopDWG SubmittalforTelephone & Data Riser Diagram	11.0	100%	100%	08 Apr 26	20Apr-26	08 Apr26 A	20Apr-26A	$000	$000	$0.00	0.0
SHOP DRAWIN GSSUBMITTALS FOR PLAYGROUND WORKS		13400	0%	0%	31 Mar 26	09Jul-26	31 Mar26 A	25Aug-26A	$000	$000	$0.00	-4000
ARCHITECTURE WORKS		3900	0%	0%	31 Mar 26	14May-26	31 Mar26 A	14May-26A	$000	$000	$0.00	0.0
MLTX02-004EN-13(	ShopDWG SubmittalforPlaygound Plan/Layout	16.0	100%	100%	31 Mar 26	18Apr-26	31 Mar26 A	18Apr-26A	$000	$000	$0.00	0.0
MLTX02-004EN-13(	ShopDWG SubmittalforFurniture& Marking	2.0	100%	100%	13 May-26	14May-26	13 May 26 A	14May-26A	$000	$000	$0.00	0.0
MLTX02-004EN-13(	ShopDWG SubmittalforSections	16.0	100%	100%	31 Mar 26	18Apr-26	31 Mar26 A	18Apr-26A	$000	$000	$0.00	0.0
MLTX02-004EN-13(	ShopDWG SubmittalforInterlockPatten Plan	7.0	100%	100%	31 Mar 26	07Apr-26	31 Mar26 A	07Apr-26A	$000	$000	$0.00	0.0
MLTX02-004EN-13(	ShopDWG SubmittalforDoors&Windows Schedule	2.0	100%	100%	13 May-26	14May-26	13 May 26 A	14May-26A	$000	$000	$0.00	0.0
MLTX02-004EN-13(	ShopDWG SubmittalforDome Internal Layout	2.0	100%	100%	13 May-26	14May-26	13 May 26 A	14May-26A	$000	$000	$0.00	0.0
STRUCTUREWORKS		2.0	0%	0%	13 May-26	14May-26	13 May 26 A	14May-26A	$000	$000	$0.00	0.0
MLTX02-004EN-13(	ShopDWG SubmittalforAir Dome System	2.0	100%	100%	13 May-26	14May-26	13 May 26 A	14May-26A	$000	$000	$0.00	0.0
MLTX02-004EN-13(	ShopDWG SubmittalforFoundationof AirDome	2.0	100%	100%	13 May-26	14May-26	13 May 26 A	14May-26A	$000	$000	$0.00	0.0
MLTX02-004EN-13(	ShopDWG SubmittalforAnchorBoltLayoutof Air Dome	2.0	100%	100%	13 May-26	14May-26	13 May 26 A	14May-26A	$000	$000	$0.00	0.0
AIRDOMESYS TEM		2.0	0%	0%	13 May-26	14May-26	13 May 26 A	14May-26A	$000	$000	$0.00	0.0
MLTX02-004EN-13(	ShopDWG SubmittalforAir Dome Stoctural Layout	2.0	100%	100%	13 May-26	14May-26	13 May 26 A	14May-26A	$000	$000	$0.00	0.0
MLTX02-004EN-13(	ShopDWG SubmittalforMembrane PanelLayout	2.0	100%	100%	13 May-26	14May-26	13 May 26 A	14May-26A	$000	$000	$0.00	0.0
MLTX02-004EN-13(	ShopDWG SubmittalforCableTension Layout	2.0	100%	100%	13 May-26	14May-26	13 May 26 A	14May-26A	$000	$000	$0.00	0.0
MLTX02-004EN-13(	ShopDWG SubmittalforAirlock DoorDetails	2.0	100%	100%	13 May-26	14May-26	13 May 26 A	14May-26A	$000	$000	$0.00	0.0
MLTX02-004EN-13(	ShopDWG SubmittalforEmergency ExitDetails	2.0	100%	100%	13 May-26	14May-26	13 May 26 A	14May-26A	$000	$000	$0.00	0.0
SPORTS EQUIPMENT		2.0	0%	0%	13 May-26	14May-26	13 May 26 A	14May-26A	$000	$000	$0.00	0.0
MLTX02-004EN-13(	ShopDWG SubmittalforFootball Turf Instalation	2.0	100%	100%	13 May-26	14May-26	13 May 26 A	14May-26A	$000	$000	$0.00	0.0
MLTX02-004EN-13(	ShopDWG SubmittalforBasketballCourtMarking	2.0	100%	100%	13 May-26	14May-26	13 May 26 A	14May-26A	$000	$000	$0.00	0.0
MLTX02-004EN-13(	ShopDWG SubmittalforPadelCourtStructure	2.0	100%	100%	13 May-26	14May-26	13 May 26 A	14May-26A	$000	$000	$0.00	0.0
MECHANCAL WORKS		2000	0%	0%	08 Apr 26	30Apr-26	08 Apr26 A	30Apr-26A	$000	$000	$0.00	0.0
MLTX02-004EN-13(	ShopDWG SubmittalforHVAC Plan	2000	100%	100%	08 Apr 26	30Apr-26	08 Apr26 A	30Apr-26A	$000	$000	$0.00	0.0
MLTX02-004EN-13(	ShopDWG SubmittalforExhaustAirPlan	2000	100%	100%	08 Apr 26	30Apr-26	08 Apr26 A	30Apr-26A	$000	$000	$0.00	0.0
ELECTRCAL WORKS		9100	0%	0%	20 May-26	09Jul-26	20 May 26 A	25Aug-26A	$000	$000	$0.00	-4000
MLTX02-004EN-12(	ShopDWG SubmittalforLighting layout	1.0	100%	100%	20 May-26	20May-26	20 May 26 A	20May-26A	$000	$000	$0.00	0.0
MLTX02-004EN-12(	ShopDWG SubmittalforPower layout	1.0	100%	100%	01 Jul-26	01Jul-26	01 Jul -26A	01Jul-26A	$000	$000	$0.00	0.0
MLTX02-004EN-12(	ShopDWG SubmittalforPower SingleLineDiagram	1.0	100%	100%	01 Jul-26	01Jul-26	01 Jul -26A	01Jul-26A	$000	$000	$0.00	0.0
MLTX02-004EN-12(	ShopDWG SubmittalforPanelBoardSchedules	1.0	100%	100%	01 Jul-26	01Jul-26	01 Jul -26A	01Jul-26A	$000	$000	$0.00	0.0
MLTX02-004EN-12(	ShopDWG SubmittalforPower Instalation Details	1.0	100%	100%	01 Jul-26	01Jul-26	01 Jul -26A	01Jul-26A	$000	$000	$0.00	0.0
MLTX02-004EN-12(	ShopDWG SubmittalforFireAlarmInstallation Details	1.0	100%	100%	23 May-26	23May-26	23 May 26 A	23May-26A	$000	$000	$0.00	0.0
MLTX02-004EN-12(	ShopDWG SubmittalforCCTV Details	4.0	100%	100%	05 Jul-26	08Jul-26	25 Aug 26 A	25Aug-26A	$000	$000	$0.00	3.0
MLTX02-004EN-12(	ShopDWG SubmittalforFireAlarmLayout	1.0	100%	100%	23 May-26	23May-26	23 May 26 A	23May-26A	$000	$000	$0.00	0.0
MLTX02-004EN-13(	ShopDWG SubmittalforFireAlarmRiserDiagram	1.0	100%	100%	23 May-26	23May-26	23 May 26 A	23May-26A	$000	$000	$0.00	0.0
MLTX02-004EN-13(	ShopDWG SubmittalforCCTV Layout	5.0	100%	100%	05 Jul-26	09Jul-26	25 Aug 26 A	25Aug-26A	$000	$000	$0.00	4.0
MLTX02-004EN-13(	ShopDWG SubmittalforCCTV Riser Diagram	5.0	100%	100%	05 Jul-26	09Jul-26	25 Aug 26 A	25Aug-26A	$000	$000	$0.00	4.0
SHOP DRAWIN GSSUBMITTALS FOR LANDSCAPE WORKS		6500	0%	0%	31 Mar 26	17Jun-26	31 Mar26 A	17Jun-26A	$000	$000	$0.00	0.0

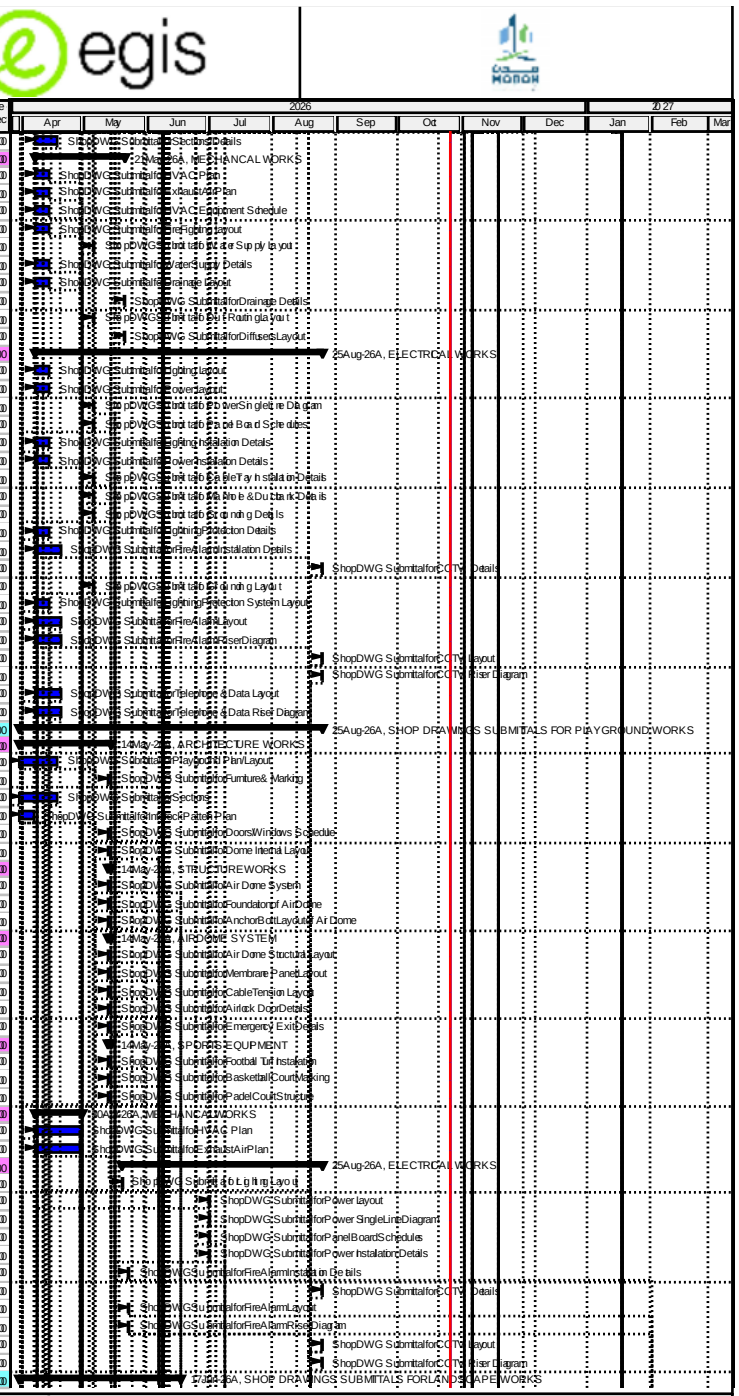

© Oracle Corporation

ActivityID	ActivityName	Orginal Duration	Schedule %	Performance% Complete	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Variance - BL Project
	ARCHITECTURE WORKS	4200	0%	0%	31 Mar 26	18-May-26	31 Mar 26 A	18May-26A	$000	$000	$0.00	0.00
MLTX02-004EN-128	ShopDWG SubmittalforLandscape Layout	2000	100%	100%	31 Mar 26	22Apr-26	31 Mar 26 A	22Apr-26A	$000	$000	$0.00	0.00
MLTX02-004EN-128	ShopDWG SubmittalforHardscape Plan	5.00	100%	100%	13 May-26	18-May-26	13 May 26 A	18May-26A	$000	$000	$0.00	0.00
MLTX02-004EN-128	ShopDWG SubmittalforPlanting Plan	5.00	100%	100%	13 May-26	18-May-26	13 May 26 A	18May-26A	$000	$000	$0.00	0.00
MLTX02-004EN-128	ShopDWG SubmittalforLandscape Details	5.00	100%	100%	13 May-26	18-May-26	13 May 26 A	18May-26A	$000	$000	$0.00	0.00
	MECHANCAL WORKS	1.00	0%	0%	17 Jun 26	17Jun-26	17 Jun 26 A	17Jun-26A	$000	$000	$0.00	0.00
MLTX02-004EN-125	ShopDWG SubmittalforIrrigation Details	1.00	100%	100%	17 Jun 26	17Jun-26	17 Jun 26 A	17Jun-26A	$000	$000	$0.00	0.00
MLTX02-004EN-125	ShopDWG SubmittalforIrrigation Layout	1.00	100%	100%	17 Jun 26	17Jun-26	17 Jun 26 A	17Jun-26A	$000	$000	$0.00	0.00
	ELECTRCAL WORKS	1.00	0%	0%	23 May-26	23May-26	23 May 26 A	23May-26A	$000	$000	$0.00	0.00
MLTX02-004EN-121	ShopDWG SubmittalforLighting GeneralArrangement	1.00	100%	100%	23 May-26	23May-26	23 May 26 A	23May-26A	$000	$000	$0.00	0.00
MLTX02-004EN-121	ShopDWG SubmittalforLighting NetworkLayout	1.00	100%	100%	23 May-26	23May-26	23 May 26 A	23May-26A	$000	$000	$0.00	0.00
MLTX02-004EN-121	ShopDWG SubmittalforLighting Details	1.00	100%	100%	23 May-26	23May-26	23 May 26 A	23May-26A	$000	$000	$0.00	0.00
MLTX02-004EN-121	ShopDWG SubmittalforLighting SingleLine Diagram	1.00	100%	100%	23 May-26	23May-26	23 May 26 A	23May-26A	$000	$000	$0.00	0.00
	SHOP DRAWINGS APPROVALS	13800	0%	0%	07 Apr 26	21Jul-26	07 Apr 26 A	26Aug-26A	$000	$000	$0.00	-3100
	SHOP DRAWIN GAPPROVALFOR EARTHINGW ORKS	6500	0%	0%	07 Apr 26	24Jun-26	07 Apr 26 A	24Jun-26A	$000	$000	$0.00	0.00
MLTX02-004EN-15530	ShopDWG Appovalfor layoutPlan	4.00	100%	100%	22 Apr 26	26Apr-26	22 Apr 26 A	26Apr-26A	$000	$000	$0.00	0.00
MLTX02-004EN-15540	ShopDWG Appovalfor SettingOut	1700	100%	100%	07 Apr 26	26Apr-26	07 Apr 26 A	26Apr-26A	$000	$000	$0.00	0.00
MLTX02-004EN-15550	ShopDWG Appovalfor GadingLayoutPlan	1.00	100%	100%	26 Apr 26	26Apr-26	26 Apr 26 A	26Apr-26A	$000	$000	$0.00	0.00
MLTX02-004EN-15560	ShopDWG Appovalfor Cub SettingOut Points	1.00	100%	100%	21 May-26	21May-26	21 May 26 A	21May-26A	$000	$000	$0.00	0.00
MLTX02-004EN-15570	ShopDWG Appovalfor Signing& Marking Layout Plan	1.00	100%	100%	24 Jun 26	24Jun-26	24 Jun 26 A	24Jun-26A	$000	$000	$0.00	0.00
MLTX02-004EN-15580	ShopDWG Appovalfor Standards Details	1.00	100%	100%	21 May-26	21May-26	21 May 26 A	21May-26A	$000	$000	$0.00	0.00
	SHOP DRAWIN GAPPROVALFOR SERVIC EDILIETWORKS	13200	0%	0%	14 Apr 26	21Jul-26	14 Apr 26 A	26Aug-26A	$000	$000	$0.00	-3100
	ARCHITECTURE WORKS	9.00	0%	0%	14 Apr 26	23Apr-26	14 Apr 26 A	24Apr-26A	$000	$000	$0.00	0.00
MLTX02-004EN-15(	ShopDWG Appovalfor RoofPlan	9.00	100%	100%	14 Apr 26	23Apr-26	14 Apr 26 A	24Apr-26A	$000	$000	$0.00	0.00
MLTX02-004EN-15(	ShopDWG Appovalfor Elevations	9.00	100%	100%	14 Apr 26	23Apr-26	14 Apr 26 A	24Apr-26A	$000	$000	$0.00	0.00
MLTX02-004EN-15(	ShopDWG Appovalfor Sections	9.00	100%	100%	14 Apr 26	23Apr-26	14 Apr 26 A	24Apr-26A	$000	$000	$0.00	0.00
MLTX02-004EN-15(	ShopDWG Appovalfor CeilingPlan	5.00	100%	100%	14 Apr 26	19Apr-26	14 Apr 26 A	19Apr-26A	$000	$000	$0.00	0.00
MLTX02-004EN-15(	ShopDWG Appovalfor finishes Plan	9.00	100%	100%	14 Apr 26	23Apr-26	14 Apr 26 A	24Apr-26A	$000	$000	$0.00	0.00
MLTX02-004EN-15(	ShopDWG Appovalfor ToiletDetails	9.00	100%	100%	14 Apr 26	23Apr-26	14 Apr 26 A	24Apr-26A	$000	$000	$0.00	0.00
MLTX02-004EN-15(	ShopDWG Appovalfor Doors/WindowsSchedule	9.00	100%	100%	14 Apr 26	23Apr-26	14 Apr 26 A	24Apr-26A	$000	$000	$0.00	0.00
	STRUCTUREWORKS	6.00	0%	0%	18 Apr 26	23Apr-26	18 Apr 26 A	23Apr-26A	$000	$000	$0.00	0.00
MLTX02-004EN-157	ShopDWG Appovalfor foundation Plan	6.00	100%	100%	18 Apr 26	23Apr-26	18 Apr 26 A	23Apr-26A	$000	$000	$0.00	0.00
MLTX02-004EN-157	ShopDWG Appovalfor Ground floorFraming Plan	6.00	100%	100%	18 Apr 26	23Apr-26	18 Apr 26 A	23Apr-26A	$000	$000	$0.00	0.00
MLTX02-004EN-157	ShopDWG Appovalfor SectionsDetails	6.00	100%	100%	18 Apr 26	23Apr-26	18 Apr 26 A	23Apr-26A	$000	$000	$0.00	0.00
	MECHANCAL WORKS	1400	0%	0%	06 May-26	21May-26	06 May 26 A	21May-26A	$000	$000	$0.00	0.00
MLTX02-004EN-157	ShopDWG Appovalfor HVACPlan	1.00	100%	100%	06 May-26	06May-26	06 May 26 A	06May-26A	$000	$000	$0.00	0.00
MLTX02-004EN-157	ShopDWG Appovalfor ExhaustAir Plan	1.00	100%	100%	07 May-26	07May-26	07 May 26 A	07May-26A	$000	$000	$0.00	0.00
MLTX02-004EN-157	ShopDWG Appovalfor HVACEquipment Schedule	1.00	100%	100%	06 May-26	06May-26	06 May 26 A	06May-26A	$000	$000	$0.00	0.00
MLTX02-004EN-157	ShopDWG Appovalfor fire fighting Layout	1.00	100%	100%	07 May-26	07May-26	07 May 26 A	07May-26A	$000	$000	$0.00	0.00
MLTX02-004EN-157	ShopDWG Appovalfor WaterSupplyLayout	0.00	100%	100%	07 May-26	07May-26	07 May 26 A	07May-26A	$000	$000	$0.00	0.00
MLTX02-004EN-157	ShopDWG Appovalfor WaterSupplyDetails	1.00	100%	100%	07 May-26	07May-26	07 May 26 A	07May-26A	$000	$000	$0.00	0.00
MLTX02-004EN-157	ShopDWG Appovalfor DrainageLayout	1.00	100%	100%	07 May-26	07May-26	07 May 26 A	07May-26A	$000	$000	$0.00	0.00
MLTX02-004EN-158	ShopDWG Appovalfor DrainageDetails	1.00	100%	100%	21 May-26	21May-26	21 May 26 A	21May-26A	$000	$000	$0.00	0.00
MLTX02-004EN-163	ShopDWG Appovalfor Duct RoutingLayout	1.00	100%	100%	07 May-26	07May-26	07 May 26 A	07May-26A	$000	$000	$0.00	0.00
MLTX02-004EN-163	ShopDWG Appovalfor Diffusers Layout	1.00	100%	100%	21 May-26	21May-26	21 May 26 A	21May-26A	$000	$000	$0.00	0.00
	ELECTRCAL WORKS	13100	0%	0%	15 Apr 26	21Jul-26	15 Apr 26 A	26Aug-26A	$000	$000	$0.00	-3100
MLTX02-004EN-158	ShopDWG Appovalfor lighting Layout	1000	100%	100%	15 Apr 26	26Apr-26	15 Apr 26 A	26Apr-26A	$000	$000	$0.00	0.00
MLTX02-004EN-158	ShopDWG Appovalfor Power Layout	1000	100%	100%	15 Apr 26	26Apr-26	15 Apr 26 A	26Apr-26A	$000	$000	$0.00	0.00
MLTX02-004EN-158	ShopDWG Appovalfor Power Single line Diagram	1.00	100%	100%	23 May-26	23May-26	23 May 26 A	23May-26A	$000	$000	$0.00	0.00
MLTX02-004EN-158	ShopDWG Appovalfor Panel Board Schedules	1.00	100%	100%	23 May-26	23May-26	23 May 26 A	23May-26A	$000	$000	$0.00	0.00
MLTX02-004EN-158	ShopDWG Appovalfor lighting InstallationDetails	1000	100%	100%	15 Apr 26	26Apr-26	15 Apr 26 A	26Apr-26A	$000	$000	$0.00	0.00
MLTX02-004EN-158	ShopDWG Appovalfor Power InstallationDetails	1000	100%	100%	15 Apr 26	26Apr-26	15 Apr 26 A	26Apr-26A	$000	$000	$0.00	0.00
MLTX02-004EN-158	ShopDWG Appovalfor Cable Tray InstallationDetails	1.00	100%	100%	23 May-26	23May-26	23 May 26 A	23May-26A	$000	$000	$0.00	0.00
MLTX02-004EN-158	ShopDWG Appovalfor Manhole& Ducttank Details	1.00	100%	100%	23 May-26	23May-26	23 May 26 A	23May-26A	$000	$000	$0.00	0.00
MLTX02-004EN-158	ShopDWG Appovalfor Grounding Details	1.00	100%	100%	23 May-26	23May-26	23 May 26 A	23May-26A	$000	$000	$0.00	0.00
MLTX02-004EN-158	ShopDWG Appovalfor lightning Potection Details	1000	100%	100%	15 Apr 26	26Apr-26	15 Apr 26 A	26Apr-26A	$000	$000	$0.00	0.00
MLTX02-004EN-158	ShopDWG Appovalfor fire Alarm Instalation Details	6.00	100%	100%	21 Apr 26	27Apr-26	21 Apr 26 A	27Apr-26A	$000	$000	$0.00	0.00
MLTX02-004EN-158	ShopDWG Appovalfor CCTV Details	8.00	100%	100%	13 Jul-26	21Jul-26	26 Aug 26 A	26Aug-26A	$000	$000	$0.00	7.00
MLTX02-004EN-158	ShopDWG Appovalfor Gounding Layout	1.00	100%	100%	23 May-26	23May-26	23 May 26 A	23May-26A	$000	$000	$0.00	0.00
MLTX02-004EN-158	ShopDWG Appovalfor lightning Potection System Layout	1000	100%	100%	15 Apr 26	26Apr-26	15 Apr 26 A	26Apr-26A	$000	$000	$0.00	0.00
MLTX02-004EN-158	ShopDWG Appovalfor fire Alarm layout	6.00	100%	100%	21 Apr 26	27Apr-26	21 Apr 26 A	27Apr-26A	$000	$000	$0.00	0.00
MLTX02-004EN-158	ShopDWG Appovalfor fire Alarm Riser Diagram	6.00	100%	100%	21 Apr 26	27Apr-26	21 Apr 26 A	27Apr-26A	$000	$000	$0.00	0.00
MLTX02-004EN-158	ShopDWG Appovalfor CCTV Layout	8.00	100%	100%	13 Jul-26	21Jul-26	26 Aug 26 A	26Aug-26A	$000	$000	$0.00	7.00
MLTX02-004EN-158	ShopDWG Appovalfor CCTV RiserDiagram	1000	100%	100%	11 Jul-26	21Jul-26	26 Aug 26 A	26Aug-26A	$000	$000	$0.00	9.00
MLTX02-004EN-158	ShopDWG Appovalfor Telephone & Data Layout	6.00	100%	100%	21 Apr 26	27Apr-26	21 Apr 26 A	27Apr-26A	$000	$000	$0.00	0.00
MLTX02-004EN-160	ShopDWG Appovalfor Telephone & Data Riser Diagram	7.00	100%	100%	20 Apr 26	27Apr-26	20 Apr 26 A	27Apr-26A	$000	$000	$0.00	0.00
	SHOP DRAWIN GSAPPROVALFOR PLAYGROUND WORKS	13700	0%	0%	08 Apr 26	21Jul-26	08 Apr 26 A	26Aug-26A	$000	$000	$0.00	-3100
	ARCHITECTURE WORKS	5400	0%	0%	08 Apr 26	13Jun-26	08 Apr 26 A	13Jun-26A	$000	$000	$0.00	0.00
MLTX02-004EN-161	ShopDWG Appovalfor Playground Plan/Layout	5.00	100%	100%	19 Apr 26	23Apr-26	19 Apr 26 A	24Apr-26A	$000	$000	$0.00	0.00
MLTX02-004EN-161	ShopDWG Appovalfor Furniture & Marking	1.00	100%	100%	13 Jun 26	13Jun-26	13 Jun 26 A	13Jun-26A	$000	$000	$0.00	0.00
MLTX02-004EN-161	ShopDWG Appovalfor Sections	5.00	100%	100%	19 Apr 26	23Apr-26	19 Apr 26 A	24Apr-26A	$000	$000	$0.00	0.00

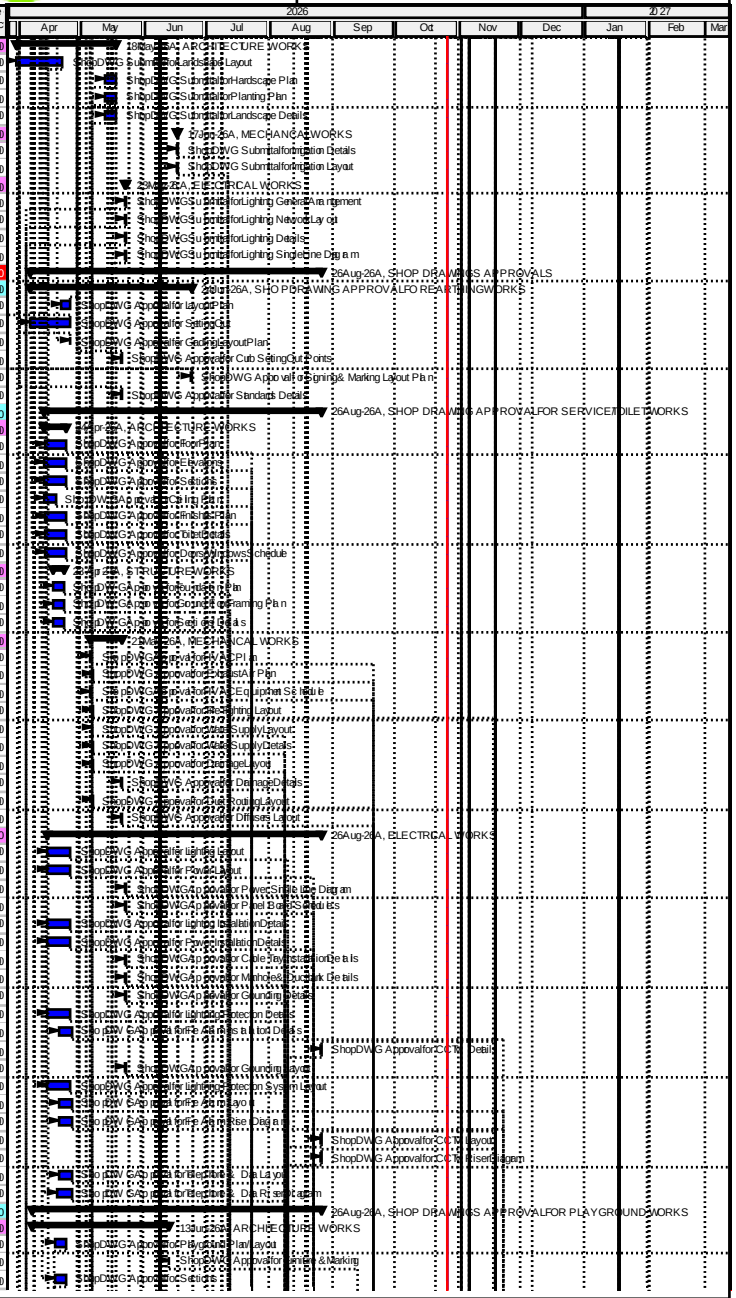


© Oracle Corporation

ActivityID	ActivityName	Orginal Duration	Schedule %	Performance% Complete	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Variance - BL Project
MLTX02-004EN-162	ShopDWG Appovalfor Interlock PatternPlan	1000	100%	100%	08 Apr 26	19Apr-26	08 Apr 26A	19Apr-26A	$000	$000	$0.00	0.00
MLTX02-004EN-162	ShopDWG Appovalfor Doors/WindowsSchedule	1.00	100%	100%	13 Jun 26	13Jun-26	13 Jun 26A	13Jun-26A	$000	$000	$0.00	0.00
MLTX02-004EN-162	ShopDWG Appovalfor Dome InternalLayout	1.00	100%	100%	13 Jun 26	13Jun-26	13 Jun 26A	13Jun-26A	$000	$000	$0.00	0.00
STRUCTUREWORKS		1.00	0%	0%	24 Jun 26	24Jun-26	24 Jun 26A	24Jun-26A	$000	$000	$0.00	0.00
MLTX02-004EN-162	ShopDWG Appovalfor Air DomeSystem	1.00	100%	100%	24 Jun 26	24Jun-26	24 Jun 26A	24Jun-26A	$000	$000	$0.00	0.00
MLTX02-004EN-162	ShopDWG Appovalfor Foundation ofAirDome	1.00	100%	100%	24 Jun 26	24Jun-26	24 Jun 26A	24Jun-26A	$000	$000	$0.00	0.00
MLTX02-004EN-162	ShopDWG Appovalfor Foundation ofAirDome	1.00	100%	100%	24 Jun 26	24Jun-26	24 Jun 26A	24Jun-26A	$000	$000	$0.00	0.00
MLTX02-004EN-162	ShopDWG Appovalfor Anchor Bolt layoutof AirDome	1.00	100%	100%	24 Jun 26	24Jun-26	24 Jun 26A	24Jun-26A	$000	$000	$0.00	0.00
AIRDOMESYS TEM		1.00	0%	0%	13 Jun 26	13Jun-26	13 Jun 26A	13Jun-26A	$000	$000	$0.00	0.00
MLTX02-004EN-162	ShopDWG Appovalfor Air DomeStructuralLayout	1.00	100%	100%	13 Jun 26	13Jun-26	13 Jun 26A	13Jun-26A	$000	$000	$0.00	0.00
MLTX02-004EN-162	ShopDWG Appovalfor MembranePanelLayout	1.00	100%	100%	13 Jun 26	13Jun-26	13 Jun 26A	13Jun-26A	$000	$000	$0.00	0.00
MLTX02-004EN-162	ShopDWG Appovalfor Cable TensionLayout	1.00	100%	100%	13 Jun 26	13Jun-26	13 Jun 26A	13Jun-26A	$000	$000	$0.00	0.00
MLTX02-004EN-162	ShopDWG Appovalfor AirlockDoorDetails	1.00	100%	100%	13 Jun 26	13Jun-26	13 Jun 26A	13Jun-26A	$000	$000	$0.00	0.00
MLTX02-004EN-162	ShopDWG Appovalfor EmergencyExitDetails	1.00	100%	100%	13 Jun 26	13Jun-26	13 Jun 26A	13Jun-26A	$000	$000	$0.00	0.00
SPORTS EQUIPMENT		1.00	0%	0%	13 Jun 26	13Jun-26	13 Jun 26A	13Jun-26A	$000	$000	$0.00	0.00
MLTX02-004EN-162	ShopDWG Appovalfor Football Tuf Installation	1.00	100%	100%	13 Jun 26	13Jun-26	13 Jun 26A	13Jun-26A	$000	$000	$0.00	0.00
MLTX02-004EN-162	ShopDWG Appovalfor Basketball Court Marking	1.00	100%	100%	13 Jun 26	13Jun-26	13 Jun 26A	13Jun-26A	$000	$000	$0.00	0.00
MLTX02-004EN-162	ShopDWG Appovalfor Padel Court Stucture	1.00	100%	100%	13 Jun 26	13Jun-26	13 Jun 26A	13Jun-26A	$000	$000	$0.00	0.00
MECHANCALWORKS		2.00	0%	0%	06 May-26	07May-26	06 May 26A	07May-26A	$000	$000	$0.00	0.00
MLTX02-004EN-161	ShopDWG Appovalfor HVACPlan	1.00	100%	100%	06 May-26	06May-26	06 May 26A	06May-26A	$000	$000	$0.00	0.00
MLTX02-004EN-161	ShopDWG Appovalfor ExhaustAir Plan	1.00	100%	100%	07 May-26	07May-26	07 May 26A	07May-26A	$000	$000	$0.00	0.00
ELECTRCALWORKS		13100	0%	0%	15 Apr 26	21Jul-26	15 Apr 26A	26Aug-26A	$000	$000	$0.00	-3100
MLTX02-004EN-160	ShopDWG Appovalfor Lighting Layout	1000	100%	100%	15 Apr 26	26Apr-26	15 Apr 26A	26Apr-26A	$000	$000	$0.00	0.00
MLTX02-004EN-160	ShopDWG Appovalfor Power Layout	1000	100%	100%	15 Apr 26	26Apr-26	15 Apr 26A	26Apr-26A	$000	$000	$0.00	0.00
MLTX02-004EN-160	ShopDWG Appovalfor Power Single line Diagram	6.00	100%	100%	05 Jul-26	11Jul-26	15 Jul -26A	15Jul-26A	$000	$000	$0.00	5.00
MLTX02-004EN-161	ShopDWG Appovalfor Panel Board Schedules	6.00	100%	100%	05 Jul-26	11Jul-26	15 Jul -26A	15Jul-26A	$000	$000	$0.00	5.00
MLTX02-004EN-161	ShopDWG Appovalfor Power InstallationDetails	6.00	100%	100%	05 Jul-26	11Jul-26	15 Jul -26A	15Jul-26A	$000	$000	$0.00	5.00
MLTX02-004EN-161	ShopDWG Appovalfor CCTV Details	1000	100%	100%	09 Jul-26	20Jul-26	26 Aug 26 A	26Aug-26A	$000	$000	$0.00	9.00
MLTX02-004EN-161	ShopDWG Appovalfor CCTV Layout	1000	100%	100%	11 Jul-26	21Jul-26	26 Aug 26 A	26Aug-26A	$000	$000	$0.00	9.00
MLTX02-004EN-161	ShopDWG Appovalfor CCTV RiserDiagram	1000	100%	100%	11 Jul-26	21Jul-26	26 Aug 26 A	26Aug-26A	$000	$000	$0.00	9.00
SHOP DRAWIN GSAPPROVALFOR LANDSCAPE WORKS		8700	0%	0%	11 Apr 26	11Jul-26	11 Apr 26A	18Jul-26A	$000	$000	$0.00	-600
ARCHITECTURE WORKS		2000	0%	0%	22 Apr 26	14May-26	22 Apr 26A	14May-26A	$000	$000	$0.00	0.00
MLTX02-004EN-160	ShopDWG Appovalfor landscape Layout	4.00	100%	100%	22 Apr 26	26Apr-26	22 Apr 26A	26Apr-26A	$000	$000	$0.00	0.00
MLTX02-004EN-160	ShopDWG Appovalfor Hardscape Plan	2.00	100%	100%	13 May-26	14May-26	13 May 26 A	14May-26A	$000	$000	$0.00	0.00
MLTX02-004EN-160	ShopDWG Appovalfor Planting Plan	2.00	100%	100%	13 May-26	14May-26	13 May 26 A	14May-26A	$000	$000	$0.00	0.00
MLTX02-004EN-160	ShopDWG Appovalfor landscape Details	2.00	100%	100%	13 May-26	14May-26	13 May 26 A	14May-26A	$000	$000	$0.00	0.00
MECHANCALWORKS		6.00	0%	0%	05 Jul-26	11Jul-26	18 Jul -26A	18Jul-26A	$000	$000	$0.00	5.00
MLTX02-004EN-160	ShopDWG Appovalfor IrrigationDetails	6.00	100%	100%	05 Jul-26	11Jul-26	18 Jul -26A	18Jul-26A	$000	$000	$0.00	5.00
MLTX02-004EN-160	ShopDWG Appovalfor IrrigationLayout	6.00	100%	100%	05 Jul-26	11Jul-26	18 Jul -26A	18Jul-26A	$000	$000	$0.00	5.00
ELECTRCALWORKS		3700	0%	0%	11 Apr 26	23May-26	11 Apr 26A	23May-26A	$000	$000	$0.00	0.00
MLTX02-004EN-159	ShopDWG Appovalfor lighting General Arrangement	1000	100%	100%	11 Apr 26	21Apr-26	11 Apr 26A	21Apr-26A	$000	$000	$0.00	0.00
MLTX02-004EN-159	ShopDWG Appovalfor lighting Network Layout	1000	100%	100%	11 Apr 26	21Apr-26	11 Apr 26A	21Apr-26A	$000	$000	$0.00	0.00
MLTX02-004EN-159	ShopDWG Appovalfor lighting Details	1000	100%	100%	11 Apr 26	21Apr-26	11 Apr 26A	21Apr-26A	$000	$000	$0.00	0.00
MLTX02-004EN-159	ShopDWG Appovalfor lighting Single Line Diagram	1.00	100%	100%	23 May-26	23May-26	23 May 26 A	23May-26A	$000	$000	$0.00	0.00
METHOD STATEMENTS		19100	0%	0%	31 Mar 26	21Jul-26	31 Mar 26A	12Nov-26	$000	$000	$0.00	-9700
METHOD STATEMENTS UBMITTAL		18100	0%	0%	31 Mar 26	21Jul-26	31 Mar 26A	01Nov-26	$000	$000	$0.00	-8700
CIVLWORKS		4500	0%	0%	31 Mar 26	21May-26	31 Mar 26A	21May-26A	$000	$000	$0.00	0.00
MLTX02-004EN-12200	Preparation & Submissionof MethodStatement forEarthwork	1700	100%	100%	31 Mar 26	19Apr-26	31 Mar 26A	19Apr-26A	$000	$000	$0.00	0.00
MLTX02-004EN-12210	Preparation & Submissionof MethodStatement forConcete Works	1.00	100%	100%	21 May-26	21May-26	21 May 26 A	21May-26A	$000	$000	$0.00	0.00
MLTX02-004EN-12220	Preparation & Submissionof MethodStatement forWaterproding	2200	100%	100%	31 Mar 26	25Apr-26	31 Mar 26A	25Apr-26A	$000	$000	$0.00	0.00
ARCHITECTURE WORKS		13200	0%	0%	31 May-26	11Jul-26	31 May 26 A	01Nov-26	$000	$000	$0.00	-9600
MLTX02-004EN-12330	Preparation & Submissionof MethodStatement forFenceWorks	5.00	0%	0%	05 Jul-26	09Jul-26	27 Oct 26	01Nov-26	$000	$000	$0.00	0.00
MLTX02-004EN-12250	Preparation & Submissionof MethodStatement forPlasteringWorks	1.00	100%	100%	16 Jun 26	16Jun-26	16 Jun 26A	16Jun-26A	$000	$000	$0.00	0.00
MLTX02-004EN-12260	Preparation & Submissionof MethodStatement forMasonary Works	1.00	100%	100%	16 Jun 26	16Jun-26	16 Jun 26A	16Jun-26A	$000	$000	$0.00	0.00
MLTX02-004EN-12270	Preparation & Submissionof MethodStatement forTilingWorks	1.00	100%	100%	06 Jun 26	06Jun-26	06 Jun 26A	06Jun-26A	$000	$000	$0.00	0.00
MLTX02-004EN-12280	Preparation & Submissionof MethodStatement forSeatsBenchesWorks	1.00	100%	100%	18 Jun 26	18Jun-26	18 Jun 26A	18Jun-26A	$000	$000	$0.00	0.00
MLTX02-004EN-12290	Preparation & Submissionof MethodStatement forDoorsWindows Works	1.00	100%	100%	06 Jun 26	06Jun-26	06 Jun 26A	06Jun-26A	$000	$000	$0.00	0.00
MLTX02-004EN-12300	Preparation & Submissionof MethodStatement forInterlock/Curbstone Works	1.00	100%	100%	31 May-26	31May-26	31 May 26 A	31May-26A	$000	$000	$0.00	0.00
MLTX02-004EN-12310	Preparation & Submissionof MethodStatement forParking Works	1.00	100%	100%	31 May-26	31May-26	31 May 26 A	31May-26A	$000	$000	$0.00	0.00
MLTX02-004EN-12320	Preparation & Submissionof MethodStatement forSoftScapeWorks	5.00	100%	100%	05 Jul-26	09Jul-26	11 Jul -26A	11Jul-26A	$000	$000	$0.00	4.00
MLTX02-004EN-12340	Preparation & Submissionof MethodStatement forAirDome Works	5.00	100%	100%	05 Jul-26	09Jul-26	19 Aug 26 A	19Aug-26A	$000	$000	$0.00	4.00
MLTX02-004EN-12350	Preparation & Submissionof MethodStatement forMetalWorks	6.00	100%	100%	05 Jul-26	11Jul-26	11 Jul -26A	11Jul-26A	$000	$000	$0.00	5.00
MLTX02-004EN-12360	Preparation & Submissionof MethodStatement forPartitions Works	5.00	100%	100%	05 Jul-26	09Jul-26	15 Jul -26A	15Jul-26A	$000	$000	$0.00	4.00
MLTX02-004EN-12370	Preparation & Submissionof MethodStatement forGypsumBoardWorks	1.00	100%	100%	14 Jun 26	14Jun-26	14 Jun 26A	14Jun-26A	$000	$000	$0.00	0.00
MECHANICALWORKS		4800	0%	0%	07 Apr 26	04Jun-26	07 Apr 26A	04Jun-26A	$000	$000	$0.00	0.00
MLTX02-004EN-12380	Preparation & Submissionof MethodStatement forSewageDrainage System	1.00	100%	100%	31 May-26	31May-26	31 May 26 A	31May-26A	$000	$000	$0.00	0.00
MLTX02-004EN-12390	Preparation & Submissionof MethodStatement forWater Supply System	1.00	100%	100%	04 Jun 26	04Jun-26	04 Jun 26A	04Jun-26A	$000	$000	$0.00	0.00
MLTX02-004EN-12400	Preparation & Submissionof MethodStatement forFire FightingSystem	7.00	100%	100%	07 Apr 26	14Apr-26	07 Apr 26A	14Apr-26A	$000	$000	$0.00	0.00
MLTX02-004EN-12410	Preparation & Submissionof MethodStatement forIrrigation System	1.00	100%	100%	04 Jun 26	04Jun-26	04 Jun 26A	04Jun-26A	$000	$000	$0.00	0.00
MLTX02-004EN-12420	Preparation & Submissionof MethodStatement forHVAC System	1.00	100%	100%	04 Jun 26	04Jun-26	04 Jun 26A	04Jun-26A	$000	$000	$0.00	0.00
ELECTRCALWORKS		4900	0%	0%	13 Jun 26	21Jul-26	13 Jun 26A	22Jul-26A	$000	$000	$0.00	-100



© Oracle Corporation


ActivityID	ActivityName	Orginal Duration	Schedule %	Performance% Complete	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Variance - BL Project
MLTX02004EN-12230	Preparation & Submissionof MethodStatement forElecticalConduits/PullingWorks	1.00	100%	100%	16 Jun 26	16Jun-26	16 Jun 26 A	16Jun-26A	$000	$000	$0.00	0.00
MLTX02004EN-12240	Preparation & Submissionof MethodStatement forLightingPoles Installation	1.00	100%	100%	17 Jun 26	17Jun-26	17 Jun 26 A	17Jun-26A	$000	$000	$0.00	0.00
MLTX02004EN-12430	Preparation & Submissionof MethodStatement forTelecommunication& DataSyste	1000	100%	100%	11 Jul-26	21Jul-26	15 Jul-26A	15Jul-26A	$000	$000	$0.00	9.00
MLTX02004EN-12440	Preparation & Submissionof MethodStatement forCCTV System	1000	100%	100%	11 Jul-26	21Jul-26	22 Jul-26A	22Jul-26A	$000	$000	$0.00	9.00
MLTX02004EN-12450	Preparation & Submissionof MethodStatement forLightingWorks	1.00	100%	100%	18 Jun 26	18Jun-26	18 Jun 26 A	18Jun-26A	$000	$000	$0.00	0.00
MLTX02004EN-12460	Preparation & Submissionof MethodStatement forEarthing/Lightning Works	1.00	100%	100%	13 Jun 26	13Jun-26	13 Jun 26 A	13Jun-26A	$000	$000	$0.00	0.00
MLTX02004EN-12470	Preparation & Submissionof MethodStatement forPanelBoards/Works	9.00	100%	100%	05 Jul-26	14Jul-26	18 Jul-26A	18Jul-26A	$000	$000	$0.00	8.00
METHOD STATEMENT APPROVAL		17800	0%	0%	15 Apr 26	21Jul-26	15 Apr26 A	12Nov-26	$000	$000	$0.00	-9700
CIVL WORKS		6.00	0%	0%	21 May-26	31May-26	21 May 26 A	31May-26A	$000	$000	$0.00	0.00
MLTX02004EN-15260	Appoval of Method Statementfor Earthwok	1.00	100%	100%	21 May-26	21May-26	21 May 26 A	21May-26A	$000	$000	$0.00	0.00
MLTX02004EN-15270	Appoval of Method Statementfor Concrete Works	1.00	100%	100%	31 May-26	31May-26	31 May 26 A	31May-26A	$000	$000	$0.00	0.00
MLTX02004EN-15280	Appoval of Method Statementfor Wateproofing	1.00	100%	100%	31 May-26	31May-26	31 May 26 A	31May-26A	$000	$000	$0.00	0.00
ARCHITECTURE WORKS		14200	0%	0%	31 May-26	21Jul-26	31 May 26 A	12Nov-26	$000	$000	$0.00	-9700
MLTX02004EN-15390	Appoval of Method Statementfor Rence Works	1000	100%	0%	11 Jul-26	21Jul-26	02 Nov 26	12Nov-26	$000	$000	$0.00	0.00
MLTX02004EN-15310	Appoval of Method Statementfor Plasteing Works	1.00	100%	100%	18 Jun 26	18Jun-26	18 Jun 26 A	18Jun-26A	$000	$000	$0.00	0.00
MLTX02004EN-15320	Appoval of Method Statementfor MasonaryWorks	1.00	100%	100%	18 Jun 26	18Jun-26	18 Jun 26 A	18Jun-26A	$000	$000	$0.00	0.00
MLTX02004EN-15330	Appoval of Method Statementfor Tiling Wwks	1.00	100%	100%	06 Jun 26	06Jun-26	06 Jun 26 A	06Jun-26A	$000	$000	$0.00	0.00
MLTX02004EN-15340	Appoval of Method Statementfor Seats/Benches Works	6.00	100%	100%	05 Jul-26	11Jul-26	11 Jul-26A	11Jul-26A	$000	$000	$0.00	5.00
MLTX02004EN-15350	Appoval of Method Statementfor Doors/WndowsWorks	1.00	100%	100%	06 Jun 26	06Jun-26	06 Jun 26 A	06Jun-26A	$000	$000	$0.00	0.00
MLTX02004EN-15360	Appoval of Method Statementfor Intelock/Cubstore Works	1.00	100%	100%	31 May-26	31May-26	31 May 26 A	31May-26A	$000	$000	$0.00	0.00
MLTX02004EN-15370	Appoval of Method Statementfor ParkingWorks	1.00	100%	100%	31 May-26	31May-26	31 May 26 A	31May-26A	$000	$000	$0.00	0.00
MLTX02004EN-15380	Appoval of Method Statementfor Soft Scape Works	1000	100%	100%	11 Jul-26	21Jul-26	11 Jul-26A	11Jul-26A	$000	$000	$0.00	9.00
MLTX02004EN-15400	Appoval of Method Statementfor Air DomeWorks	1000	100%	100%	11 Jul-26	21Jul-26	27 Aug 26 A	27Aug-26A	$000	$000	$0.00	9.00
MLTX02004EN-15410	Appoval of Method Statementfor PartitionsWorks	1000	100%	100%	11 Jul-26	21Jul-26	15 Jul-26A	15Jul-26A	$000	$000	$0.00	9.00
MLTX02004EN-15420	Appoval of Method Statementfor Gypsum Board Wwks	1.00	100%	100%	18 Jun 26	18Jun-26	18 Jun 26 A	18Jun-26A	$000	$000	$0.00	0.00
MECHANICALWORKS		4700	0%	0%	15 Apr 26	11Jun-26	15 Apr26 A	11Jun-26A	$000	$000	$0.00	0.00
MLTX02004EN-15430	Appoval of Method Statementfor Sewage/DainageSystem	1.00	100%	100%	11 Jun 26	11Jun-26	11 Jun 26 A	11Jun-26A	$000	$000	$0.00	0.00
MLTX02004EN-15440	Appoval of Method Statementfor WaterSupplySystem	1.00	100%	100%	11 Jun 26	11Jun-26	11 Jun 26 A	11Jun-26A	$000	$000	$0.00	0.00
MLTX02004EN-15450	Appoval of Method Statementfor FireFighting System	1000	100%	100%	15 Apr 26	26Apr-26	15 Apr26 A	26Apr-26A	$000	$000	$0.00	0.00
MLTX02004EN-15460	Appoval of Method Statementfor IrigationSystem	1.00	100%	100%	11 Jun 26	11Jun-26	11 Jun 26 A	11Jun-26A	$000	$000	$0.00	0.00
MLTX02004EN-15470	Appoval of Method Statementfor H/AC System	1.00	100%	100%	11 Jun 26	11Jun-26	11 Jun 26 A	11Jun-26A	$000	$000	$0.00	0.00
ELECTRCAL W ORKS		2100	0%	0%	05 Jul-26	21Jul-26	11 Jul-26A	22Jul-26A	$000	$000	$0.00	4.00
MLTX02004EN-15290	Appoval of Method Statementfor ElecticalConduits/Pulling Works	6.00	100%	100%	05 Jul-26	11Jul-26	11 Jul-26A	11Jul-26A	$000	$000	$0.00	5.00
MLTX02004EN-15300	Appoval of Method Statementfor Lighting Poles Installaion	1000	100%	100%	05 Jul-26	15Jul-26	11 Jul-26A	11Jul-26A	$000	$000	$0.00	9.00
MLTX02004EN-15480	Appoval of Method Statementfor Telecommunication & Data System	1000	100%	100%	05 Jul-26	15Jul-26	15 Jul-26A	15Jul-26A	$000	$000	$0.00	9.00
MLTX02004EN-15490	Appoval of Method Statementfor CCTV System	1000	100%	100%	11 Jul-26	21Jul-26	22 Jul-26A	22Jul-26A	$000	$000	$0.00	9.00
MLTX02004EN-15500	Appoval of Method Statementfor Lighting Works	1000	100%	100%	05 Jul-26	15Jul-26	11 Jul-26A	11Jul-26A	$000	$000	$0.00	9.00
MLTX02004EN-15510	Appoval of Method Statementfor Earthing/LightningWorks	5.00	100%	100%	05 Jul-26	09Jul-26	11 Jul-26A	11Jul-26A	$000	$000	$0.00	4.00
MLTX02004EN-15520	Appoval of Method Statementfor Panel Boards Works	5.00	100%	100%	16 Jul-26	21Jul-26	18 Jul-26A	18Jul-26A	$000	$000	$0.00	4.00
PRE-QUALRICATION& MATERIAL		18600	0%	0%	31 Mar 26	15Jul-26	31 Mar26 A	07Nov-26	$000	$000	$0.00	-9700
PRE-QUALRICATION		4500	0%	0%	31 Mar 26	21May-26	31 Mar26 A	21May-26A	$000	$000	$0.00	0.00
TOILETSERVIC EWORKS		1400	0%	0%	31 Mar 26	15Apr-26	31 Mar26 A	15Apr-26A	$000	$000	$0.00	0.00
STEELRENFORCEMENT		1200	0%	0%	31 Mar 26	13Apr-26	31 Mar26 A	13Apr-26A	$000	$000	$0.00	0.00
MLTX02004EN-142	PreQualifcation Appovalfor SteelReinfocement	2.00	100%	100%	12 Apr 26	13Apr-26	12 Apr26 A	13Apr-26A	$000	$000	$0.00	0.00
MLTX02004EN-142	PreQualifcation SubmittalforSteelReinfocement	1100	100%	100%	31 Mar 26	12Apr-26	31 Mar26 A	12Apr-26A	$000	$000	$0.00	0.00
READY MKCO NCRETE		1100	0%	0%	31 Mar 26	12Apr-26	31 Mar26 A	12Apr-26A	$000	$000	$0.00	0.00
MLTX02004EN-142	PreQualifcation SubmittalforReadyMixed Concrete	1000	100%	100%	31 Mar 26	11Apr-26	31 Mar26 A	11Apr-26A	$000	$000	$0.00	0.00
MLTX02004EN-142	PreQualifcation Appovalof Ready Mixed Concete	2.00	100%	100%	11 Apr 26	12Apr-26	11 Apr26 A	12Apr-26A	$000	$000	$0.00	0.00
CONCRETE BLOCKS		1100	0%	0%	31 Mar 26	12Apr-26	31 Mar26 A	12Apr-26A	$000	$000	$0.00	0.00
MLTX02004EN-144	PreQualifcation SubmittalforConcrete Blocks	1000	100%	100%	31 Mar 26	11Apr-26	31 Mar26 A	11Apr-26A	$000	$000	$0.00	0.00
MLTX02004EN-144	PreQualifcation Appovalfor Concrete Blocks	2.00	100%	100%	11 Apr 26	12Apr-26	11 Apr26 A	12Apr-26A	$000	$000	$0.00	0.00
WATERPROOFING		1200	0%	0%	31 Mar 26	13Apr-26	31 Mar26 A	13Apr-26A	$000	$000	$0.00	0.00
MLTX02004EN-143	PreQualifcation Appovalfor WaterProofing	3.00	100%	100%	11 Apr 26	13Apr-26	11 Apr26 A	13Apr-26A	$000	$000	$0.00	0.00
MLTX02004EN-142	PreQualifcation SubmittalforWater Proofing	1000	100%	100%	31 Mar 26	11Apr-26	31 Mar26 A	11Apr-26A	$000	$000	$0.00	0.00
FLOORWALL TILES		1100	0%	0%	31 Mar 26	12Apr-26	31 Mar26 A	12Apr-26A	$000	$000	$0.00	0.00
MLTX02004EN-145	PreQualifcation SubmittalforTiling Materials	1000	100%	100%	31 Mar 26	11Apr-26	31 Mar26 A	11Apr-26A	$000	$000	$0.00	0.00
MLTX02004EN-145	PreQualifcation Appovalfor Tailing Material	5.00	100%	100%	07 Apr 26	12Apr-26	07 Apr26 A	12Apr-26A	$000	$000	$0.00	0.00
SUSPENDED CEILING		1200	0%	0%	31 Mar 26	13Apr-26	31 Mar26 A	13Apr-26A	$000	$000	$0.00	0.00
MLTX02004EN-145	PreQualifcation SubmittalforSuspendCeiling	1100	100%	100%	31 Mar 26	12Apr-26	31 Mar26 A	12Apr-26A	$000	$000	$0.00	0.00
MLTX02004EN-145	PreQualifcation Appovalfor SuspendCeiling	2.00	100%	100%	12 Apr 26	13Apr-26	12 Apr26 A	13Apr-26A	$000	$000	$0.00	0.00
DOORS/WNDO WS		1100	0%	0%	31 Mar 26	12Apr-26	31 Mar26 A	12Apr-26A	$000	$000	$0.00	0.00
MLTX02004EN-145	PreQualifcation SubmittalforDoors/Windows	1000	100%	100%	31 Mar 26	11Apr-26	31 Mar26 A	11Apr-26A	$000	$000	$0.00	0.00
MLTX02004EN-145	PreQualifcation Appovalfor Doors/Windows	2.00	100%	100%	11 Apr 26	12Apr-26	11 Apr26 A	12Apr-26A	$000	$000	$0.00	0.00
FURNITURES		1100	0%	0%	31 Mar 26	12Apr-26	31 Mar26 A	12Apr-26A	$000	$000	$0.00	0.00
MLTX02004EN-146	PreQualifcation SubmittalforFurnitures	1000	100%	100%	31 Mar 26	11Apr-26	31 Mar26 A	11Apr-26A	$000	$000	$0.00	0.00
MLTX02004EN-146	PreQualifcation Appovalfor Furnitures	2.00	100%	100%	11 Apr 26	12Apr-26	11 Apr26 A	12Apr-26A	$000	$000	$0.00	0.00
SANITARY FIXTURES		1100	0%	0%	31 Mar 26	12Apr-26	31 Mar26 A	12Apr-26A	$000	$000	$0.00	0.00
MLTX02004EN-145	PreQualifcation SubmittalforSanitary Fixtures	1000	100%	100%	31 Mar 26	11Apr-26	31 Mar26 A	11Apr-26A	$000	$000	$0.00	0.00
MLTX02004EN-145	PreQualifcation Appovalfor Sanitay Fixtures	2.00	100%	100%	11 Apr 26	12Apr-26	11 Apr26 A	12Apr-26A	$000	$000	$0.00	0.00
WATERSUPPLY PIPES		1100	0%	0%	31 Mar 26	12Apr-26	31 Mar26 A	12Apr-26A	$000	$000	$0.00	0.00
MLTX02004EN-145	PreQualifcation SubmittalforWater Supply Pipes	1000	100%	100%	31 Mar 26	11Apr-26	31 Mar26 A	11Apr-26A	$000	$000	$0.00	0.00
MLTX02004EN-145	PreQualifcation Appovalfor WaterSupplyPipes	2.00	100%	100%	11 Apr 26	12Apr-26	11 Apr26 A	12Apr-26A	$000	$000	$0.00	0.00

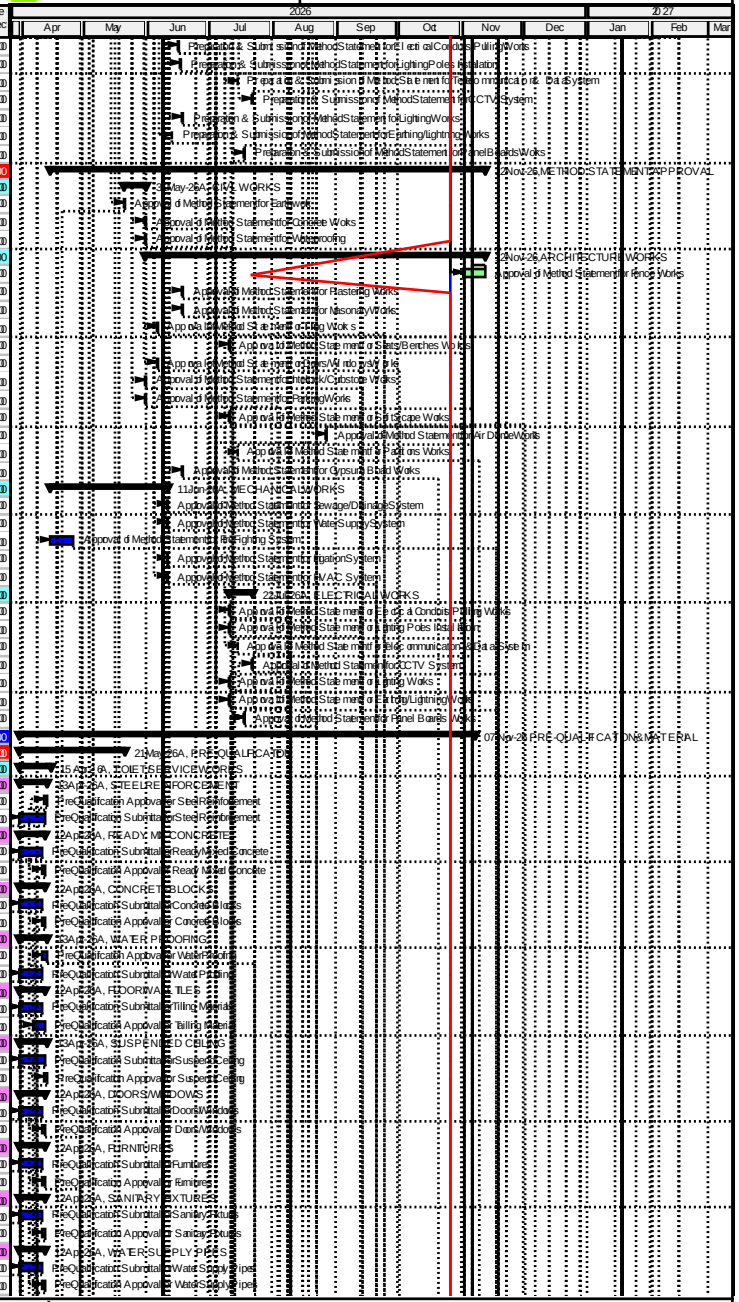

© Oracle Corporation

ActivityID	ActivityName	Orginal Duration	Schedule %	Performance% Complete	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cos	Earned Value Cos	Budgeted Tot Cos	Variance - BL Project
SEWAGEDRAINAGEPIPES		1100	0%	0%	31 Mar 26	12Apr-26	31 Mar 26 A	12Apr-26A	$000	$000	$0.00	0.00
MLTX02-004EN-146	PreQualifcation SubmittalforSewageDrainage Pipes	1000	100%	100%	31 Mar 26	11Apr-26	31 Mar 26 A	11Apr-26A	$000	$000	$0.00	0.00
MLTX02-004EN-146	PreQualifcation Appovalfor Sewage/DrainagePipes	2.00	100%	100%	11 Apr 26	12Apr-26	11 Apr 26 A	12Apr-26A	$000	$000	$0.00	0.00
PACKAGE ACUNITS		8.00	0%	0%	07 Apr 26	15Apr-26	07 Apr 26 A	15Apr-26A	$000	$000	$0.00	0.00
MLTX02-004EN-146	PreQualifcation SubmittalforPackageAC Units	6.00	100%	100%	07 Apr 26	13Apr-26	07 Apr 26 A	13Apr-26A	$000	$000	$0.00	0.00
MLTX02-004EN-147	PreQualifcation Appovalfor PackageAC Units	5.00	100%	100%	11 Apr 26	15Apr-26	11 Apr 26 A	15Apr-26A	$000	$000	$0.00	0.00
AIRDFUSSERS/GRILLS		8.00	0%	0%	07 Apr 26	15Apr-26	07 Apr 26 A	15Apr-26A	$000	$000	$0.00	0.00
MLTX02-004EN-147	PreQualifcation SubmittalforAir Diffusers/Grills	6.00	100%	100%	07 Apr 26	13Apr-26	07 Apr 26 A	13Apr-26A	$000	$000	$0.00	0.00
MLTX02-004EN-147	PreQualifcation Appovalfor Air Diffusers/Grills	5.00	100%	100%	11 Apr 26	15Apr-26	11 Apr 26 A	15Apr-26A	$000	$000	$0.00	0.00
GALVANIZEDDUCTS		8.00	0%	0%	07 Apr 26	15Apr-26	07 Apr 26 A	15Apr-26A	$000	$000	$0.00	0.00
MLTX02-004EN-147	PreQualifcation SubmittalforGalvarized Ducts	6.00	100%	100%	07 Apr 26	13Apr-26	07 Apr 26 A	13Apr-26A	$000	$000	$0.00	0.00
MLTX02-004EN-147	PreQualifcation Appovalfor Galvanized Ducts	5.00	100%	100%	11 Apr 26	15Apr-26	11 Apr 26 A	15Apr-26A	$000	$000	$0.00	0.00
EXHAUSTFANS		8.00	0%	0%	07 Apr 26	15Apr-26	07 Apr 26 A	15Apr-26A	$000	$000	$0.00	0.00
MLTX02-004EN-147	PreQualifcation SubmittalforExhaustFans	5.00	100%	100%	07 Apr 26	12Apr-26	07 Apr 26 A	12Apr-26A	$000	$000	$0.00	0.00
MLTX02-004EN-147	PreQualifcation Appovalfor ExhaustFans	5.00	100%	100%	11 Apr 26	15Apr-26	11 Apr 26 A	15Apr-26A	$000	$000	$0.00	0.00
LIGHTING FIXTURES		8.00	0%	0%	07 Apr 26	15Apr-26	07 Apr 26 A	15Apr-26A	$000	$000	$0.00	0.00
MLTX02-004EN-146	PreQualifcation SubmittalforLighting Fixtues	3.00	100%	100%	07 Apr 26	09Apr-26	07 Apr 26 A	09Apr-26A	$000	$000	$0.00	0.00
MLTX02-004EN-146	PreQualifcation Appovalfor Lighting Fixtures	5.00	100%	100%	11 Apr 26	15Apr-26	11 Apr 26 A	15Apr-26A	$000	$000	$0.00	0.00
SWITCHES/SOCKETS		8.00	0%	0%	07 Apr 26	15Apr-26	07 Apr 26 A	15Apr-26A	$000	$000	$0.00	0.00
MLTX02-004EN-146	PreQualifcation SubmittalforSwitches/Sockets	3.00	100%	100%	07 Apr 26	09Apr-26	07 Apr 26 A	09Apr-26A	$000	$000	$0.00	0.00
MLTX02-004EN-146	PreQualifcation Appovalfor Switches/Sockets	5.00	100%	100%	11 Apr 26	15Apr-26	11 Apr 26 A	15Apr-26A	$000	$000	$0.00	0.00
EARTHINGSYSTEM		8.00	0%	0%	07 Apr 26	15Apr-26	07 Apr 26 A	15Apr-26A	$000	$000	$0.00	0.00
MLTX02-004EN-144	PreQualifcation SubmittalforEarthing System	3.00	100%	100%	07 Apr 26	09Apr-26	07 Apr 26 A	09Apr-26A	$000	$000	$0.00	0.00
MLTX02-004EN-144	PreQualifcation Appovalfor Earthing System	5.00	100%	100%	11 Apr 26	15Apr-26	11 Apr 26 A	15Apr-26A	$000	$000	$0.00	0.00
DISTRBUTION PANNELS		8.00	0%	0%	07 Apr 26	15Apr-26	07 Apr 26 A	15Apr-26A	$000	$000	$0.00	0.00
MLTX02-004EN-144	PreQualifcation SubmittalforDistibution Panels	3.00	100%	100%	07 Apr 26	09Apr-26	07 Apr 26 A	09Apr-26A	$000	$000	$0.00	0.00
MLTX02-004EN-144	PreQualifcation Appovalfor Distribution Panels	5.00	100%	100%	11 Apr 26	15Apr-26	11 Apr 26 A	15Apr-26A	$000	$000	$0.00	0.00
PLAYGROUND WORKS		1400	0%	0%	31 Mar 26	15Apr-26	31 Mar 26 A	15Apr-26A	$000	$000	$0.00	0.00
PVC MEMBRANE		1400	0%	0%	31 Mar 26	15Apr-26	31 Mar 26 A	15Apr-26A	$000	$000	$0.00	0.00
MLTX02-004EN-148	PreQualifcation SubmittalforPVC Membane	1200	100%	100%	31 Mar 26	13Apr-26	31 Mar 26 A	13Apr-26A	$000	$000	$0.00	0.00
MLTX02-004EN-148	PreQualifcation Appovalfor PVCMembrane	3.00	100%	100%	13 Apr 26	15Apr-26	13 Apr 26 A	15Apr-26A	$000	$000	$0.00	0.00
STEELTENSION CABLES		1400	0%	0%	31 Mar 26	15Apr-26	31 Mar 26 A	15Apr-26A	$000	$000	$0.00	0.00
MLTX02-004EN-148	PreQualifcation SubmittalforSteelTension Cables	1200	100%	100%	31 Mar 26	13Apr-26	31 Mar 26 A	13Apr-26A	$000	$000	$0.00	0.00
MLTX02-004EN-151	PreQualifcation Appovalfor SteelTensionCables	3.00	100%	100%	13 Apr 26	15Apr-26	13 Apr 26 A	15Apr-26A	$000	$000	$0.00	0.00
EMERGENCY DOORS		1400	0%	0%	31 Mar 26	15Apr-26	31 Mar 26 A	15Apr-26A	$000	$000	$0.00	0.00
MLTX02-004EN-148	PreQualifcation SubmittalforEmergency Doors	1200	100%	100%	31 Mar 26	13Apr-26	31 Mar 26 A	13Apr-26A	$000	$000	$0.00	0.00
MLTX02-004EN-151	PreQualifcation Appovalfor EmargencyDoors	3.00	100%	100%	13 Apr 26	15Apr-26	13 Apr 26 A	15Apr-26A	$000	$000	$0.00	0.00
PRESSURE UNITS		1400	0%	0%	31 Mar 26	15Apr-26	31 Mar 26 A	15Apr-26A	$000	$000	$0.00	0.00
MLTX02-004EN-148	PreQualifcation SubmittalforPressue Units	1200	100%	100%	31 Mar 26	13Apr-26	31 Mar 26 A	13Apr-26A	$000	$000	$0.00	0.00
MLTX02-004EN-151	PreQualifcation Appovalfor Pressue Units	3.00	100%	100%	13 Apr 26	15Apr-26	13 Apr 26 A	15Apr-26A	$000	$000	$0.00	0.00
AIRLOCK DOORS		1400	0%	0%	31 Mar 26	15Apr-26	31 Mar 26 A	15Apr-26A	$000	$000	$0.00	0.00
MLTX02-004EN-148	PreQualifcation SubmittalforLockDoors	1200	100%	100%	31 Mar 26	13Apr-26	31 Mar 26 A	13Apr-26A	$000	$000	$0.00	0.00
MLTX02-004EN-152	PreQualifcation Appovalfor lock Doos	3.00	100%	100%	13 Apr 26	15Apr-26	13 Apr 26 A	15Apr-26A	$000	$000	$0.00	0.00
ARTFICIAL TURF		1100	0%	0%	31 Mar 26	12Apr-26	31 Mar 26 A	12Apr-26A	$000	$000	$0.00	0.00
MLTX02-004EN-150	PreQualifcation SubmittalforArtificial TURF	1000	100%	100%	31 Mar 26	11Apr-26	31 Mar 26 A	11Apr-26A	$000	$000	$0.00	0.00
MLTX02-004EN-152	PreQualifcation Appovalfor ArtificalTURF	2.00	100%	100%	11 Apr 26	12Apr-26	11 Apr 26 A	12Apr-26A	$000	$000	$0.00	0.00
RUBBER GRANULES		1400	0%	0%	31 Mar 26	15Apr-26	31 Mar 26 A	15Apr-26A	$000	$000	$0.00	0.00
MLTX02-004EN-150	PreQualifcation SubmittalforRubberGranules	1200	100%	100%	31 Mar 26	13Apr-26	31 Mar 26 A	13Apr-26A	$000	$000	$0.00	0.00
MLTX02-004EN-152	PreQualifcation Appovalfor RubberGranules	3.00	100%	100%	13 Apr 26	15Apr-26	13 Apr 26 A	15Apr-26A	$000	$000	$0.00	0.00
PADEL GIASS		1400	0%	0%	31 Mar 26	15Apr-26	31 Mar 26 A	15Apr-26A	$000	$000	$0.00	0.00
MLTX02-004EN-150	PreQualifcation SubmittalforPadelGlass	1200	100%	100%	31 Mar 26	13Apr-26	31 Mar 26 A	13Apr-26A	$000	$000	$0.00	0.00
MLTX02-004EN-152	PreQualifcation Appovalfor Padel Glass	3.00	100%	100%	13 Apr 26	15Apr-26	13 Apr 26 A	15Apr-26A	$000	$000	$0.00	0.00
PADEL WIREMESH/STEELSETS		1400	0%	0%	31 Mar 26	15Apr-26	31 Mar 26 A	15Apr-26A	$000	$000	$0.00	0.00
MLTX02-004EN-150	PreQualifcation SubmittalforWireMesh/SteelSets	1200	100%	100%	31 Mar 26	13Apr-26	31 Mar 26 A	13Apr-26A	$000	$000	$0.00	0.00
MLTX02-004EN-152	PreQualifcation Appovalfor WireMesh/Steel Sets	3.00	100%	100%	13 Apr 26	15Apr-26	13 Apr 26 A	15Apr-26A	$000	$000	$0.00	0.00
AGGREGATE BASECOURSE		1400	0%	0%	31 Mar 26	15Apr-26	31 Mar 26 A	15Apr-26A	$000	$000	$0.00	0.00
MLTX02-004EN-143	PreQualifcation SubmittalforAggregate Base Course	1200	100%	100%	31 Mar 26	13Apr-26	31 Mar 26 A	13Apr-26A	$000	$000	$0.00	0.00
MLTX02-004EN-143	PreQualifcation Appovalfor Aggregate BaseCourse	3.00	100%	100%	13 Apr 26	15Apr-26	13 Apr 26 A	15Apr-26A	$000	$000	$0.00	0.00
BITUMNOUS BASE &WEARING COURSE		7.00	0%	0%	07 Apr 26	14Apr-26	07 Apr 26 A	14Apr-26A	$000	$000	$0.00	0.00
MLTX02-004EN-143	PreQualifcation SubmittalforBituminous Base & WearingCource	5.00	100%	100%	07 Apr 26	12Apr-26	07 Apr 26 A	12Apr-26A	$000	$000	$0.00	0.00
MLTX02-004EN-143	PreQualifcation Appovalfor he Site	3.00	100%	100%	12 Apr 26	14Apr-26	12 Apr 26 A	14Apr-26A	$000	$000	$0.00	0.00
INTERLOCKING PAVING		2.00	0%	0%	11 Apr 26	12Apr-26	11 Apr 26 A	12Apr-26A	$000	$000	$0.00	0.00
MLTX02-004EN-144	PreQualifcation Appovalfor Interbcking BlockPavers	2.00	100%	100%	11 Apr 26	12Apr-26	11 Apr 26 A	12Apr-26A	$000	$000	$0.00	0.00
MLTX02-004EN-143	PreQualifcation SubmittalforIntelocking Block Paves	1.00	100%	100%	11 Apr 26	11Apr-26	11 Apr 26 A	11Apr-26A	$000	$000	$0.00	0.00
MARKINGPAINT		8.00	0%	0%	04 Apr 26	12Apr-26	04 Apr 26 A	12Apr-26A	$000	$000	$0.00	0.00
MLTX02-004EN-146	PreQualifcation SubmittalforMarking Paint	8.00	100%	100%	04 Apr 26	12Apr-26	04 Apr 26 A	12Apr-26A	$000	$000	$0.00	0.00
MLTX02-004EN-152	PreQualifcation Appovalfor MakingPaint	1.00	100%	100%	12 Apr 26	12Apr-26	12 Apr 26 A	12Apr-26A	$000	$000	$0.00	0.00
PACKAGE ACUNITS		1100	0%	0%	04 Apr 26	15Apr-26	04 Apr 26 A	15Apr-26A	$000	$000	$0.00	0.00
MLTX02-004EN-147	PreQualifcation SubmittalforPackageAC Units	9.00	100%	100%	04 Apr 26	13Apr-26	04 Apr 26 A	13Apr-26A	$000	$000	$0.00	0.00
MLTX02-004EN-147	PreQualifcation Appovalfor PackageAC Units	3.00	100%	100%	13 Apr 26	15Apr-26	13 Apr 26 A	15Apr-26A	$000	$000	$0.00	0.00
AIRDFUSSERS/GRILLS		1100	0%	0%	04 Apr 26	15Apr-26	04 Apr 26 A	15Apr-26A	$000	$000	$0.00	0.00
MLTX02-004EN-147	PreQualifcation SubmittalforAir Dffussers/Grills	9.00	100%	100%	04 Apr 26	13Apr-26	04 Apr 26 A	13Apr-26A	$000	$000	$0.00	0.00


© Oracle Corporation

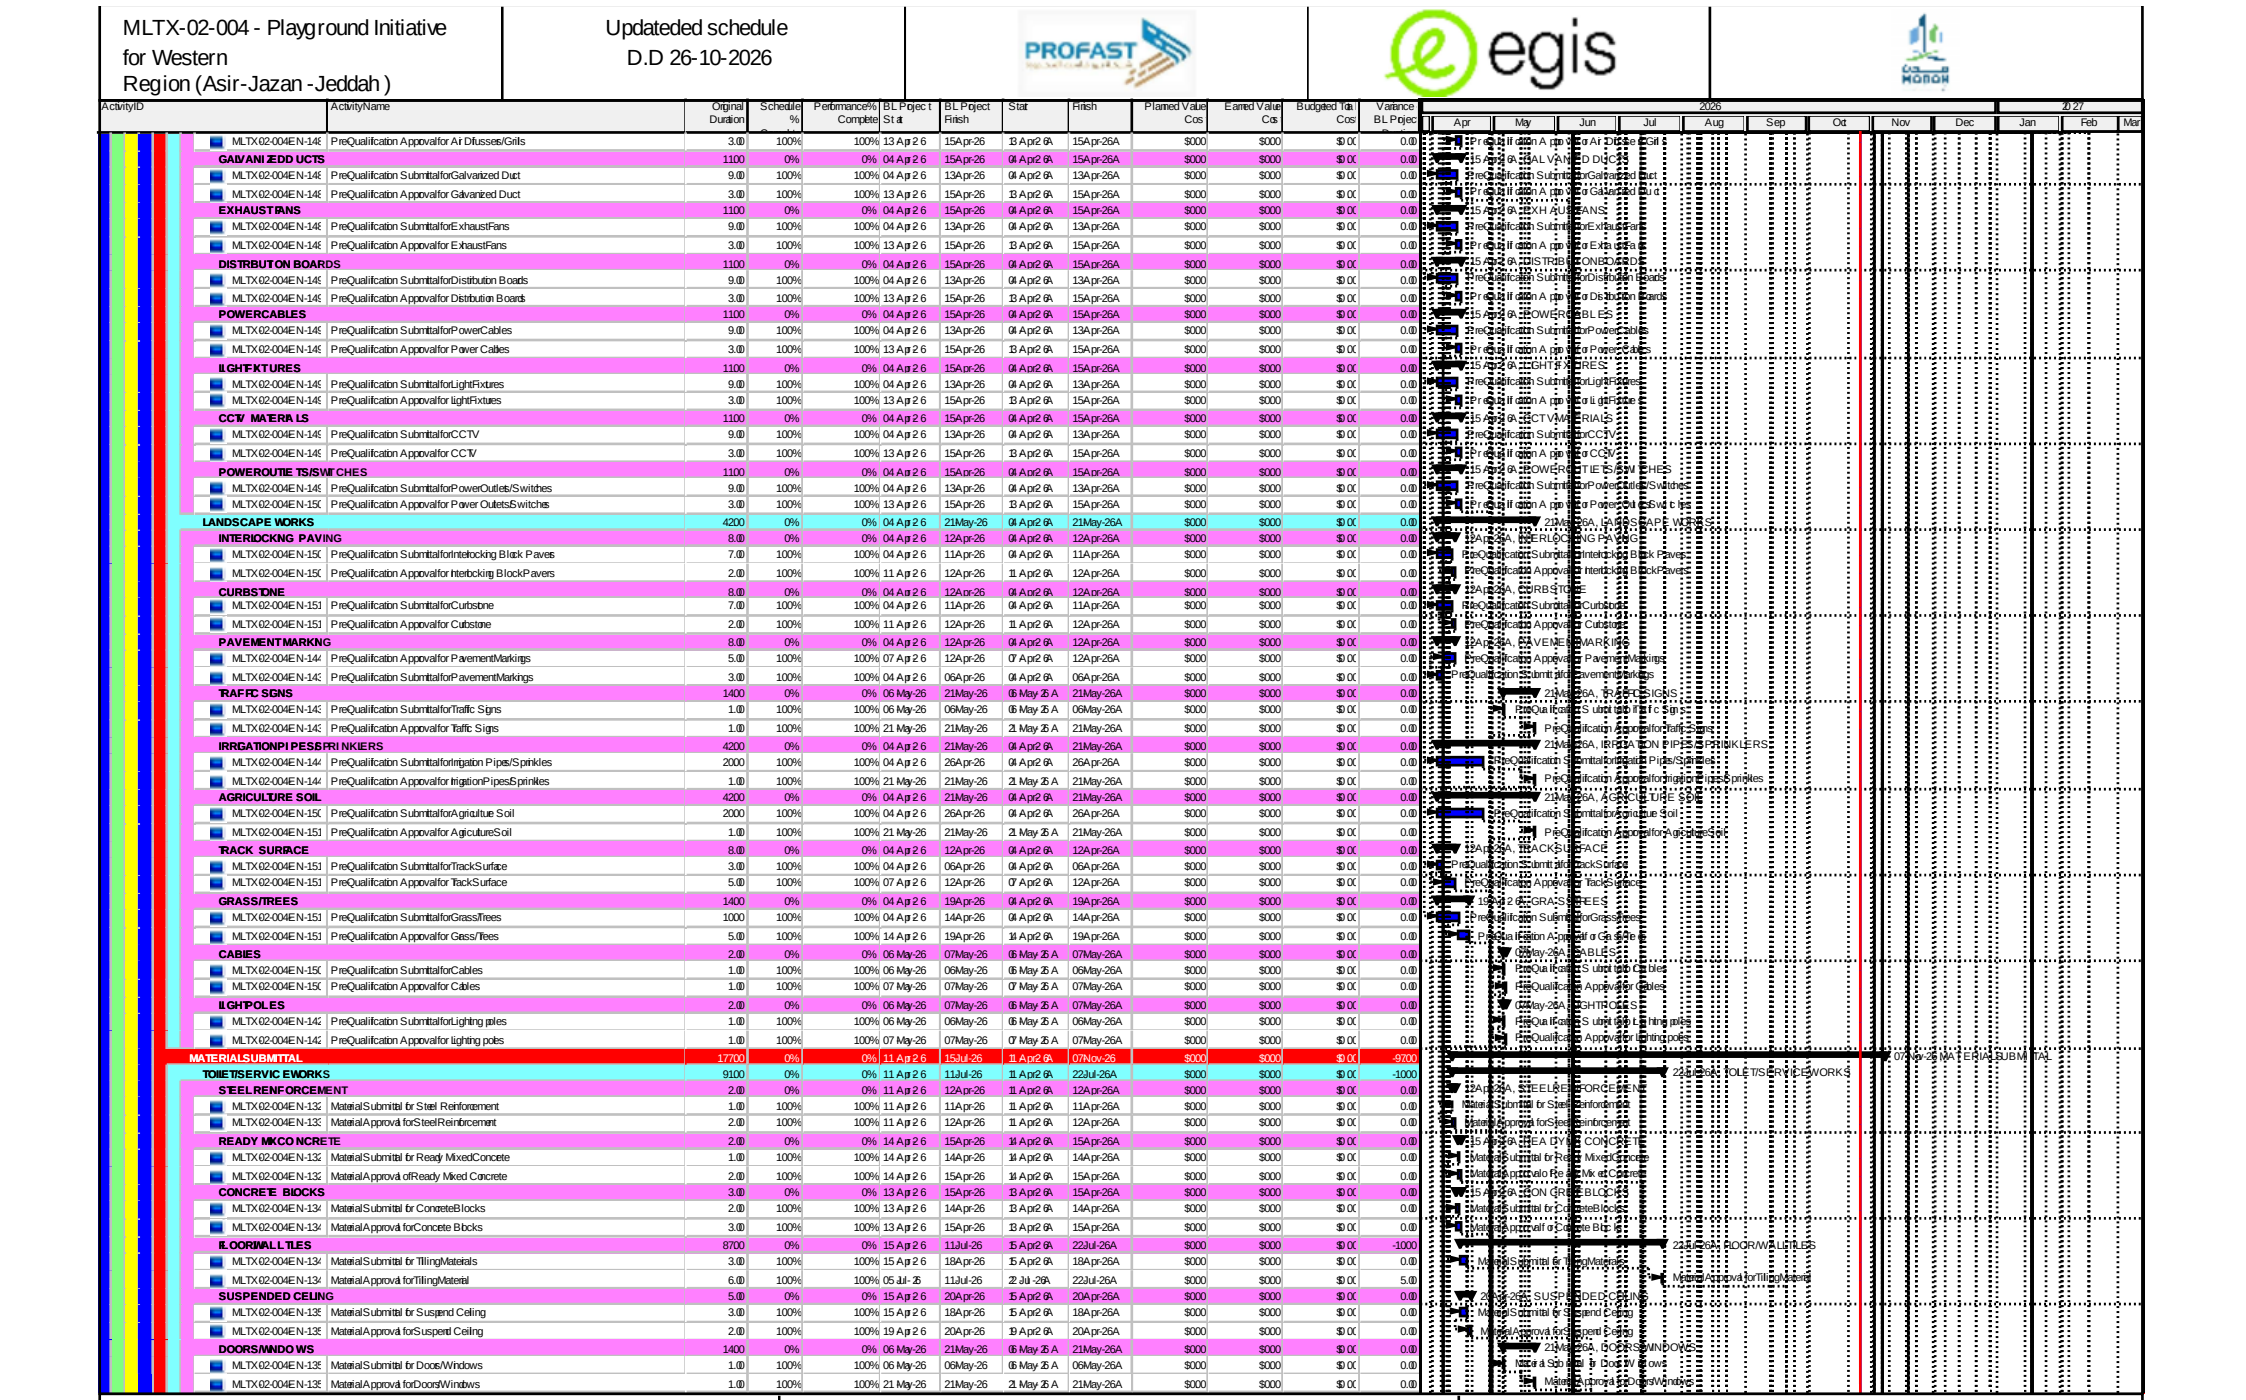

ActivityID	ActivityName	Orginal Duration	Schedule %	Performance% Complete	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Variance - BL Project
MLTX02-004EN-148	PreQualifcation Approval for Air Difusses/Grills	3.0d	100%	100%	13 Apr 26	15Apr-26	13 Apr 26 A	15Apr-26A	$000	$000	$0.00	0.0d
GALVANIZEDDUCTS		1100	0%	0%	04 Apr 26	15Apr-26	04 Apr 26 A	15Apr-26A	$000	$000	$0.00	0.0d
MLTX02-004EN-148	PreQualifcation Submittal for Galvarized Duct	9.0d	100%	100%	04 Apr 26	13Apr-26	04 Apr 26 A	13Apr-26A	$000	$000	$0.00	0.0d
MLTX02-004EN-148	PreQualifcation Approval for Galvanized Duct	3.0d	100%	100%	13 Apr 26	15Apr-26	13 Apr 26 A	15Apr-26A	$000	$000	$0.00	0.0d
EXHAUSTFANS		1100	0%	0%	04 Apr 26	15Apr-26	04 Apr 26 A	15Apr-26A	$000	$000	$0.00	0.0d
MLTX02-004EN-148	PreQualifcation Submittal for Exhaust Fans	9.0d	100%	100%	04 Apr 26	13Apr-26	04 Apr 26 A	13Apr-26A	$000	$000	$0.00	0.0d
MLTX02-004EN-148	PreQualifcation Approval for Exhaust Fans	3.0d	100%	100%	13 Apr 26	15Apr-26	13 Apr 26 A	15Apr-26A	$000	$000	$0.00	0.0d
DISTRBUTION BOARDS		1100	0%	0%	04 Apr 26	15Apr-26	04 Apr 26 A	15Apr-26A	$000	$000	$0.00	0.0d
MLTX02-004EN-149	PreQualifcation Submittal for Distibution Boards	9.0d	100%	100%	04 Apr 26	13Apr-26	04 Apr 26 A	13Apr-26A	$000	$000	$0.00	0.0d
MLTX02-004EN-149	PreQualifcation Approval for Distribution Boards	3.0d	100%	100%	13 Apr 26	15Apr-26	13 Apr 26 A	15Apr-26A	$000	$000	$0.00	0.0d
POWERCABLES		1100	0%	0%	04 Apr 26	15Apr-26	04 Apr 26 A	15Apr-26A	$000	$000	$0.00	0.0d
MLTX02-004EN-149	PreQualifcation Submittal for Power Cables	9.0d	100%	100%	04 Apr 26	13Apr-26	04 Apr 26 A	13Apr-26A	$000	$000	$0.00	0.0d
MLTX02-004EN-149	PreQualifcation Approval for Power Cables	3.0d	100%	100%	13 Apr 26	15Apr-26	13 Apr 26 A	15Apr-26A	$000	$000	$0.00	0.0d
LIGHTFIXTURES		1100	0%	0%	04 Apr 26	15Apr-26	04 Apr 26 A	15Apr-26A	$000	$000	$0.00	0.0d
MLTX02-004EN-149	PreQualifcation Submittal for Light Fixtures	9.0d	100%	100%	04 Apr 26	13Apr-26	04 Apr 26 A	13Apr-26A	$000	$000	$0.00	0.0d
MLTX02-004EN-149	PreQualifcation Approval for Light Fixtures	3.0d	100%	100%	13 Apr 26	15Apr-26	13 Apr 26 A	15Apr-26A	$000	$000	$0.00	0.0d
CCTV MATERIALS		1100	0%	0%	04 Apr 26	15Apr-26	04 Apr 26 A	15Apr-26A	$000	$000	$0.00	0.0d
MLTX02-004EN-149	PreQualifcation Submittal for CCTV	9.0d	100%	100%	04 Apr 26	13Apr-26	04 Apr 26 A	13Apr-26A	$000	$000	$0.00	0.0d
MLTX02-004EN-149	PreQualifcation Approval for CCTV	3.0d	100%	100%	13 Apr 26	15Apr-26	13 Apr 26 A	15Apr-26A	$000	$000	$0.00	0.0d
POWEROUTLETS/SWITCHES		1100	0%	0%	04 Apr 26	15Apr-26	04 Apr 26 A	15Apr-26A	$000	$000	$0.00	0.0d
MLTX02-004EN-149	PreQualifcation Submittal for PowerOutlets/Switches	9.0d	100%	100%	04 Apr 26	13Apr-26	04 Apr 26 A	13Apr-26A	$000	$000	$0.00	0.0d
MLTX02-004EN-150	PreQualifcation Approval for Power Outets/Switches	3.0d	100%	100%	13 Apr 26	15Apr-26	13 Apr 26 A	15Apr-26A	$000	$000	$0.00	0.0d
LANDSCAPE WORKS		4200	0%	0%	04 Apr 26	21May-26	04 Apr 26 A	21May-26A	$000	$000	$0.00	0.0d
INTERLOCKING PAVING		8.0d	0%	0%	04 Apr 26	12Apr-26	04 Apr 26 A	12Apr-26A	$000	$000	$0.00	0.0d
MLTX02-004EN-150	PreQualifcation Submittal for Interlocking Block Pavers	7.0d	100%	100%	04 Apr 26	11Apr-26	04 Apr 26 A	11Apr-26A	$000	$000	$0.00	0.0d
MLTX02-004EN-150	PreQualifcation Approval for Interlocking Block Pavers	2.0d	100%	100%	11 Apr 26	12Apr-26	11 Apr 26 A	12Apr-26A	$000	$000	$0.00	0.0d
CURBSTONE		8.0d	0%	0%	04 Apr 26	12Apr-26	04 Apr 26 A	12Apr-26A	$000	$000	$0.00	0.0d
MLTX02-004EN-151	PreQualifcation Submittal for Curbstone	7.0d	100%	100%	04 Apr 26	11Apr-26	04 Apr 26 A	11Apr-26A	$000	$000	$0.00	0.0d
MLTX02-004EN-151	PreQualifcation Approval for Cubstone	2.0d	100%	100%	11 Apr 26	12Apr-26	11 Apr 26 A	12Apr-26A	$000	$000	$0.00	0.0d
PAVEMENTMARKNG		8.0d	0%	0%	04 Apr 26	12Apr-26	04 Apr 26 A	12Apr-26A	$000	$000	$0.00	0.0d
MLTX02-004EN-144	PreQualifcation Approval for Pavement Markings	5.0d	100%	100%	07 Apr 26	12Apr-26	07 Apr 26 A	12Apr-26A	$000	$000	$0.00	0.0d
MLTX02-004EN-143	PreQualifcation Submittal for Pavement Markings	3.0d	100%	100%	04 Apr 26	06Apr-26	04 Apr 26 A	06Apr-26A	$000	$000	$0.00	0.0d
TRAFFIC SIGNS		1400	0%	0%	06 May-26	21May-26	06 May 26 A	21May-26A	$000	$000	$0.00	0.0d
MLTX02-004EN-143	PreQualifcation Submittal for Traffic Signs	1.0d	100%	100%	06 May-26	06May-26	06 May 26 A	06May-26A	$000	$000	$0.00	0.0d
MLTX02-004EN-143	PreQualifcation Approval for Traffic Signs	1.0d	100%	100%	21 May-26	21May-26	21 May 26 A	21May-26A	$000	$000	$0.00	0.0d
IRRGATIONPIPESSPRINKLERS		4200	0%	0%	04 Apr 26	21May-26	04 Apr 26 A	21May-26A	$000	$000	$0.00	0.0d
MLTX02-004EN-144	PreQualifcation Submittal for Irrigation Pipes/Sprinkles	2000	100%	100%	04 Apr 26	26Apr-26	04 Apr 26 A	26Apr-26A	$000	$000	$0.00	0.0d
MLTX02-004EN-144	PreQualifcation Approval for Irrigation Pipes/Sprinkles	1.0d	100%	100%	21 May-26	21May-26	21 May 26 A	21May-26A	$000	$000	$0.00	0.0d
AGRICULTURE SOIL		4200	0%	0%	04 Apr 26	21May-26	04 Apr 26 A	21May-26A	$000	$000	$0.00	0.0d
MLTX02-004EN-150	PreQualifcation Submittal for Agriculture Soil	2000	100%	100%	04 Apr 26	26Apr-26	04 Apr 26 A	26Apr-26A	$000	$000	$0.00	0.0d
MLTX02-004EN-151	PreQualifcation Approval for AgricutureSoil	1.0d	100%	100%	21 May-26	21May-26	21 May 26 A	21May-26A	$000	$000	$0.00	0.0d
TRACK SURFACE		8.0d	0%	0%	04 Apr 26	12Apr-26	04 Apr 26 A	12Apr-26A	$000	$000	$0.00	0.0d
MLTX02-004EN-151	PreQualifcation Submittal for Track Surface	3.0d	100%	100%	04 Apr 26	06Apr-26	04 Apr 26 A	06Apr-26A	$000	$000	$0.00	0.0d
MLTX02-004EN-151	PreQualifcation Approval for Track Surface	5.0d	100%	100%	07 Apr 26	12Apr-26	07 Apr 26 A	12Apr-26A	$000	$000	$0.00	0.0d
GRASS/TREES		1400	0%	0%	04 Apr 26	19Apr-26	04 Apr 26 A	19Apr-26A	$000	$000	$0.00	0.0d
MLTX02-004EN-151	PreQualifcation Submittal for Grass/Trees	1000	100%	100%	04 Apr 26	14Apr-26	04 Apr 26 A	14Apr-26A	$000	$000	$0.00	0.0d
MLTX02-004EN-151	PreQualifcation Approval for Gass/Trees	5.0d	100%	100%	14 Apr 26	19Apr-26	14 Apr 26 A	19Apr-26A	$000	$000	$0.00	0.0d
CABIES		2.0d	0%	0%	06 May-26	07May-26	06 May 26 A	07May-26A	$000	$000	$0.00	0.0d
MLTX02-004EN-150	PreQualifcation Submittal for Cables	1.0d	100%	100%	06 May-26	06May-26	06 May 26 A	06May-26A	$000	$000	$0.00	0.0d
MLTX02-004EN-150	PreQualifcation Approval for Cables	1.0d	100%	100%	07 May-26	07May-26	07 May 26 A	07May-26A	$000	$000	$0.00	0.0d
LIGHTPOLES		2.0d	0%	0%	06 May-26	07May-26	06 May 26 A	07May-26A	$000	$000	$0.00	0.0d
MLTX02-004EN-142	PreQualifcation Submittal for Lighting poles	1.0d	100%	100%	06 May-26	06May-26	06 May 26 A	06May-26A	$000	$000	$0.00	0.0d
MLTX02-004EN-142	PreQualifcation Approval for lighting pobs	1.0d	100%	100%	07 May-26	07May-26	07 May 26 A	07May-26A	$000	$000	$0.00	0.0d
MATERIALSUBMITTAL		17700	0%	0%	11 Apr 26	15Jul-26	11 Apr 26 A	07Nov-26	$000	$000	$0.00	-9700
TOILETSERVICEWORKS		9100	0%	0%	11 Apr 26	11Jul-26	11 Apr 26 A	22Jul-26A	$000	$000	$0.00	-1000
STEELREINFORCEMENT		2.0d	0%	0%	11 Apr 26	12Apr-26	11 Apr 26 A	12Apr-26A	$000	$000	$0.00	0.0d
MLTX02-004EN-132	Material Submittal for Steel Reinforement	1.0d	100%	100%	11 Apr 26	11Apr-26	11 Apr 26 A	11Apr-26A	$000	$000	$0.00	0.0d
MLTX02-004EN-133	Material Approval for Steel Reinforcement	2.0d	100%	100%	11 Apr 26	12Apr-26	11 Apr 26 A	12Apr-26A	$000	$000	$0.00	0.0d
READY MIXED CONCRETE		2.0d	0%	0%	14 Apr 26	15Apr-26	14 Apr 26 A	15Apr-26A	$000	$000	$0.00	0.0d
MLTX02-004EN-132	Material Submittal for Ready Mixed Concrete	1.0d	100%	100%	14 Apr 26	14Apr-26	14 Apr 26 A	14Apr-26A	$000	$000	$0.00	0.0d
MLTX02-004EN-132	Material Approval of Ready Mixed Concrete	2.0d	100%	100%	14 Apr 26	15Apr-26	14 Apr 26 A	15Apr-26A	$000	$000	$0.00	0.0d
CONCRETE BLOCKS		3.0d	0%	0%	13 Apr 26	15Apr-26	13 Apr 26 A	15Apr-26A	$000	$000	$0.00	0.0d
MLTX02-004EN-134	Material Submittal for Concrete Blocks	2.0d	100%	100%	13 Apr 26	14Apr-26	13 Apr 26 A	14Apr-26A	$000	$000	$0.00	0.0d
MLTX02-004EN-134	Material Approval for Concrete Bbcks	3.0d	100%	100%	13 Apr 26	15Apr-26	13 Apr 26 A	15Apr-26A	$000	$000	$0.00	0.0d
FLOORWALLTILES		8700	0%	0%	15 Apr 26	11Jul-26	15 Apr 26 A	22Jul-26A	$000	$000	$0.00	-1000
MLTX02-004EN-134	Material Submittal for Tiling Materials	3.0d	100%	100%	15 Apr 26	18Apr-26	15 Apr 26 A	18Apr-26A	$000	$000	$0.00	0.0d
MLTX02-004EN-134	Material Approval for Tiling Material	6.0d	100%	100%	05 Jul-26	11Jul-26	22 Jul-26A	22Jul-26A	$000	$000	$0.00	5.0d
SUSPENDED CEILING		5.0d	0%	0%	15 Apr 26	20Apr-26	15 Apr 26 A	20Apr-26A	$000	$000	$0.00	0.0d
MLTX02-004EN-135	Material Submittal for Suspend Ceiling	3.0d	100%	100%	15 Apr 26	18Apr-26	15 Apr 26 A	18Apr-26A	$000	$000	$0.00	0.0d
MLTX02-004EN-135	Material Approval for Suspend Ceiling	2.0d	100%	100%	19 Apr 26	20Apr-26	19 Apr 26 A	20Apr-26A	$000	$000	$0.00	0.0d
DOORS/WINDOWS		1400	0%	0%	06 May-26	21May-26	06 May 26 A	21May-26A	$000	$000	$0.00	0.0d
MLTX02-004EN-135	Material Submittal for Doors/Windows	1.0d	100%	100%	06 May-26	06May-26	06 May 26 A	06May-26A	$000	$000	$0.00	0.0d
MLTX02-004EN-135	Material Approval for Doors/Windows	1.0d	100%	100%	21 May-26	21May-26	21 May 26 A	21May-26A	$000	$000	$0.00	0.0d

© Oracle Corporation

ActivityID	ActivityName	Orginal Duration	Schedule %	Performance% Complete	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Variance - BL Project
FURNITURES		2.00	0%	0%	06 May-26	07May-26	06 May-26 A	07May-26A	$000	$000	$0.00	0.00
MLTX02-004EN-136	Material Submittal for Furnitures	1.00	100%	100%	06 May-26	06May-26	06 May-26 A	06May-26A	$000	$000	$0.00	0.00
MLTX02-004EN-136	Material Approval for Furnitures	1.00	100%	100%	07 May-26	07May-26	07 May-26 A	07May-26A	$000	$000	$0.00	0.00
SANITARY FIXTURES		14.00	0%	0%	15 Apr-26	30Apr-26	15 Apr-26 A	30Apr-26A	$000	$000	$0.00	0.00
MLTX02-004EN-135	Material Submittal for Sanitary Fixtures	6.00	100%	100%	15 Apr-26	21Apr-26	15 Apr-26 A	21Apr-26A	$000	$000	$0.00	0.00
MLTX02-004EN-135	Material Approval for Sanitary fixtures	11.00	100%	100%	19 Apr-26	30Apr-26	19 Apr-26 A	30Apr-26A	$000	$000	$0.00	0.00
WATER SUPPLY PIPES		2.00	0%	0%	15 Apr-26	16Apr-26	15 Apr-26 A	16Apr-26A	$000	$000	$0.00	0.00
MLTX02-004EN-135	Material Submittal for Water Supply Pipes	1.00	100%	100%	15 Apr-26	15Apr-26	15 Apr-26 A	15Apr-26A	$000	$000	$0.00	0.00
MLTX02-004EN-135	Material Approval for Water Supply Pipes	2.00	100%	100%	15 Apr-26	16Apr-26	15 Apr-26 A	16Apr-26A	$000	$000	$0.00	0.00
SEWAGE DRAINAGE PIPES		2.00	0%	0%	15 Apr-26	16Apr-26	15 Apr-26 A	16Apr-26A	$000	$000	$0.00	0.00
MLTX02-004EN-135	Material Submittal for Sewage/Drainage Pipes	1.00	100%	100%	15 Apr-26	15Apr-26	15 Apr-26 A	15Apr-26A	$000	$000	$0.00	0.00
MLTX02-004EN-135	Material Approval for Sewage Drainage Pipes	2.00	100%	100%	15 Apr-26	16Apr-26	15 Apr-26 A	16Apr-26A	$000	$000	$0.00	0.00
PACKAGE ACUNITS		2.00	0%	0%	06 May-26	07May-26	06 May-26 A	07May-26A	$000	$000	$0.00	0.00
MLTX02-004EN-136	Material Submittal for Package ACUnits	1.00	100%	100%	06 May-26	06May-26	06 May-26 A	06May-26A	$000	$000	$0.00	0.00
MLTX02-004EN-136	Material Approval for Package AC Units	1.00	100%	100%	07 May-26	07May-26	07 May-26 A	07May-26A	$000	$000	$0.00	0.00
AIRDFUSSERS/GRILLS		19.00	0%	0%	16 Apr-26	07May-26	16 Apr-26 A	07May-26A	$000	$000	$0.00	0.00
MLTX02-004EN-136	Material Submittal for AirDiffusers/Grills	6.00	100%	100%	16 Apr-26	22Apr-26	16 Apr-26 A	22Apr-26A	$000	$000	$0.00	0.00
MLTX02-004EN-137	Material Approval for AirDiffusers/Grills	1.00	100%	100%	07 May-26	07May-26	07 May-26 A	07May-26A	$000	$000	$0.00	0.00
GALVANIZED UCTS		6.00	0%	0%	13 Jun-26	18Jun-26	13 Jun-26 A	18Jun-26A	$000	$000	$0.00	0.00
MLTX02-004EN-137	Material Submittal for GalvanizedDucts	1.00	100%	100%	13 Jun-26	13Jun-26	13 Jun-26 A	13Jun-26A	$000	$000	$0.00	0.00
MLTX02-004EN-137	Material Approval for GalvanizedDucts	1.00	100%	100%	18 Jun-26	18Jun-26	18 Jun-26 A	18Jun-26A	$000	$000	$0.00	0.00
EXHAUST FANS		18.00	0%	0%	16 Apr-26	06May-26	16 Apr-26 A	06May-26A	$000	$000	$0.00	0.00
MLTX02-004EN-137	Material Submittal for Exhaust Fans	2.00	100%	100%	16 Apr-26	18Apr-26	16 Apr-26 A	18Apr-26A	$000	$000	$0.00	0.00
MLTX02-004EN-137	Material Approval for Exhaust Fans	1.00	100%	100%	06 May-26	06May-26	06 May-26 A	06May-26A	$000	$000	$0.00	0.00
LIGHTING FIXTURES		8.00	0%	0%	16 Apr-26	25Apr-26	16 Apr-26 A	25Apr-26A	$000	$000	$0.00	0.00
MLTX02-004EN-136	Material Submittal for LightingFixtures	3.00	100%	100%	16 Apr-26	19Apr-26	16 Apr-26 A	19Apr-26A	$000	$000	$0.00	0.00
MLTX02-004EN-136	Material Approval for LightingFixtues	5.00	100%	100%	20 Apr-26	25Apr-26	20 Apr-26 A	25Apr-26A	$000	$000	$0.00	0.00
SWITCHES/SOCKETS		8.00	0%	0%	16 Apr-26	25Apr-26	16 Apr-26 A	25Apr-26A	$000	$000	$0.00	0.00
MLTX02-004EN-136	Material Submittal for Switches/Sockets	3.00	100%	100%	16 Apr-26	19Apr-26	16 Apr-26 A	19Apr-26A	$000	$000	$0.00	0.00
MLTX02-004EN-136	Material Approval for Switches/Sockets	5.00	100%	100%	20 Apr-26	25Apr-26	20 Apr-26 A	25Apr-26A	$000	$000	$0.00	0.00
EARTHINGSYSTEM		2.00	0%	0%	06 May-26	07May-26	06 May-26 A	07May-26A	$000	$000	$0.00	0.00
MLTX02-004EN-134	Material Submittal for EarthingSystem	1.00	100%	100%	06 May-26	06May-26	06 May-26 A	06May-26A	$000	$000	$0.00	0.00
MLTX02-004EN-134	Material Approval for Earthing System	1.00	100%	100%	07 May-26	07May-26	07 May-26 A	07May-26A	$000	$000	$0.00	0.00
DISTRBUTON PANNELS		8.00	0%	0%	16 Apr-26	25Apr-26	16 Apr-26 A	25Apr-26A	$000	$000	$0.00	0.00
MLTX02-004EN-134	Material Submittal for DistributionPanels	3.00	100%	100%	16 Apr-26	19Apr-26	16 Apr-26 A	19Apr-26A	$000	$000	$0.00	0.00
MLTX02-004EN-134	Material Approval for Distibuton Panels	5.00	100%	100%	20 Apr-26	25Apr-26	20 Apr-26 A	25Apr-26A	$000	$000	$0.00	0.00
PLAYGROUND WORKS		176.00	0%	0%	12 Apr-26	15Jul-26	12 Apr-26 A	07Nov-26	$000	$000	$0.00	-97.00
PVC MEMBRANE		77.00	0%	0%	06 May-26	15Jul-26	06 May-26 A	27Jul-26A	$000	$000	$0.00	-10.00
MLTX02-004EN-136	Material Submittal for PVC Membrane	1.00	100%	100%	06 May-26	06May-26	06 May-26 A	06May-26A	$000	$000	$0.00	0.00
MLTX02-004EN-136	Material Approval for PVC Membane	10.00	100%	100%	05 Jul-25	15Jul-26	27 Jul-26A	27Jul-26A	$000	$000	$0.00	9.00
STEEL TENSION CABLES		155.00	0%	0%	06 May-26	15Jul-26	06 May-26 A	07Nov-26	$000	$000	$0.00	-97.00
MLTX02-004EN-141	Material Approval for Steel Tension Cables	10.00	100%	0%	05 Jul-25	15Jul-26	27 Oct26	07Nov-26	$000	$000	$0.00	0.00
MLTX02-004EN-136	Material Submittal for Steel TensionCables	1.00	100%	100%	06 May-26	06May-26	06 May-26 A	06May-26A	$000	$000	$0.00	0.00
EMERGENCY DOORS		147.00	0%	0%	06 May-26	15Jul-26	06 May-26 A	19Aug-26A	$000	$000	$0.00	-30.00
MLTX02-004EN-136	Material Submittal for Emegency Doors	1.00	100%	100%	06 May-26	06May-26	06 May-26 A	06May-26A	$000	$000	$0.00	0.00
MLTX02-004EN-141	Material Approval for Emergency Doors	10.00	100%	100%	05 Jul-25	15Jul-26	19 Aug-26 A	19Aug-26A	$000	$000	$0.00	9.00
PRESSURE UNITS		155.00	0%	0%	06 May-26	15Jul-26	06 May-26 A	07Nov-26	$000	$000	$0.00	-97.00
MLTX02-004EN-141	Material Approval for Pressure Units	10.00	100%	0%	05 Jul-25	15Jul-26	27 Oct26	07Nov-26	$000	$000	$0.00	0.00
MLTX02-004EN-136	Material Submittal for PressureUnits	1.00	100%	100%	06 May-26	06May-26	06 May-26 A	06May-26A	$000	$000	$0.00	0.00
AIRLOCK DOORS		14.00	0%	0%	06 May-26	21May-26	06 May-26 A	21May-26A	$000	$000	$0.00	0.00
MLTX02-004EN-136	Material Submittal for Lock Doors	5.00	100%	100%	06 May-26	11May-26	06 May-26 A	11May-26A	$000	$000	$0.00	0.00
MLTX02-004EN-141	Material Approval for LockDoors	10.00	100%	100%	21 May-26	21May-26	21 May-26 A	21May-26A	$000	$000	$0.00	0.00
ARTIFICIAL TURF		17.00	0%	0%	12 Apr-26	30Apr-26	12 Apr-26 A	30Apr-26A	$000	$000	$0.00	0.00
MLTX02-004EN-140	Material Submittal for Artificial TURF	15.00	100%	100%	12 Apr-26	28Apr-26	12 Apr-26 A	28Apr-26A	$000	$000	$0.00	0.00
MLTX02-004EN-141	Material Approval for Artificial TURF	3.00	100%	100%	28 Apr-26	30Apr-26	28 Apr-26 A	30Apr-26A	$000	$000	$0.00	0.00
RUBBER GRANULES		73.00	0%	0%	06 May-26	15Jul-26	06 May-26 A	22Jul-26A	$000	$000	$0.00	-60.00
MLTX02-004EN-140	Material Submittal for Rubber Granules	1.00	100%	100%	06 May-26	06May-26	06 May-26 A	06May-26A	$000	$000	$0.00	0.00
MLTX02-004EN-142	Material Approval for RubberGranules	10.00	100%	100%	05 Jul-25	15Jul-26	22 Jul-26A	22Jul-26A	$000	$000	$0.00	9.00
PADEL GLASS		14.00	0%	0%	06 May-26	21May-26	06 May-26 A	21May-26A	$000	$000	$0.00	0.00
MLTX02-004EN-140	Material Submittal for Padel Glass	1.00	100%	100%	06 May-26	06May-26	06 May-26 A	06May-26A	$000	$000	$0.00	0.00
MLTX02-004EN-142	Material Approval for PadelGlass	1.00	100%	100%	21 May-26	21May-26	21 May-26 A	21May-26A	$000	$000	$0.00	0.00
PADEL WIRE MESH/STEEL SETS		57.00	0%	0%	25 May-26	15Jul-26	25 May-26 A	22Jul-26A	$000	$000	$0.00	-60.00
MLTX02-004EN-140	Material Submittal for Wire Mesh/Steel Sets	1.00	100%	100%	25 May-26	25May-26	25 May-26 A	25May-26A	$000	$000	$0.00	0.00
MLTX02-004EN-142	Material Approval for Wie MeshSteel Sets	10.00	100%	100%	05 Jul-25	15Jul-26	22 Jul-26A	22Jul-26A	$000	$000	$0.00	9.00
AGGREGATE BASE COURSE		11.00	0%	0%	21 May-26	06Jun-26	21 May-26 A	06Jun-26A	$000	$000	$0.00	0.00
MLTX02-004EN-133	Material Submittal for AggegateBase Cairse	1.00	100%	100%	21 May-26	21May-26	21 May-26 A	21May-26A	$000	$000	$0.00	0.00
MLTX02-004EN-133	Material Approval for Aggregate Base Couse	1.00	100%	100%	06 Jun-26	06Jun-26	06 Jun-26 A	06Jun-26A	$000	$000	$0.00	0.00
BITUMNOUS BASE & WEARING COURSE		2.00	0%	0%	16 Apr-26	18Apr-26	16 Apr-26 A	18Apr-26A	$000	$000	$0.00	0.00
MLTX02-004EN-133	Material Submittal for BituminousBase& Wearing Couce	2.00	100%	100%	16 Apr-26	18Apr-26	16 Apr-26 A	18Apr-26A	$000	$000	$0.00	0.00
MLTX02-004EN-133	Material Approval for theSite	1.00	100%	100%	18 Apr-26	18Apr-26	18 Apr-26 A	18Apr-26A	$000	$000	$0.00	0.00
INTERLOCKING PAVING		1.00	0%	0%	21 May-26	21May-26	21 May-26 A	21May-26A	$000	$000	$0.00	0.00
MLTX02-004EN-133	Material Submittal for InterlockingBlockPavers	1.00	100%	100%	21 May-26	21May-26	21 May-26 A	21May-26A	$000	$000	$0.00	0.00

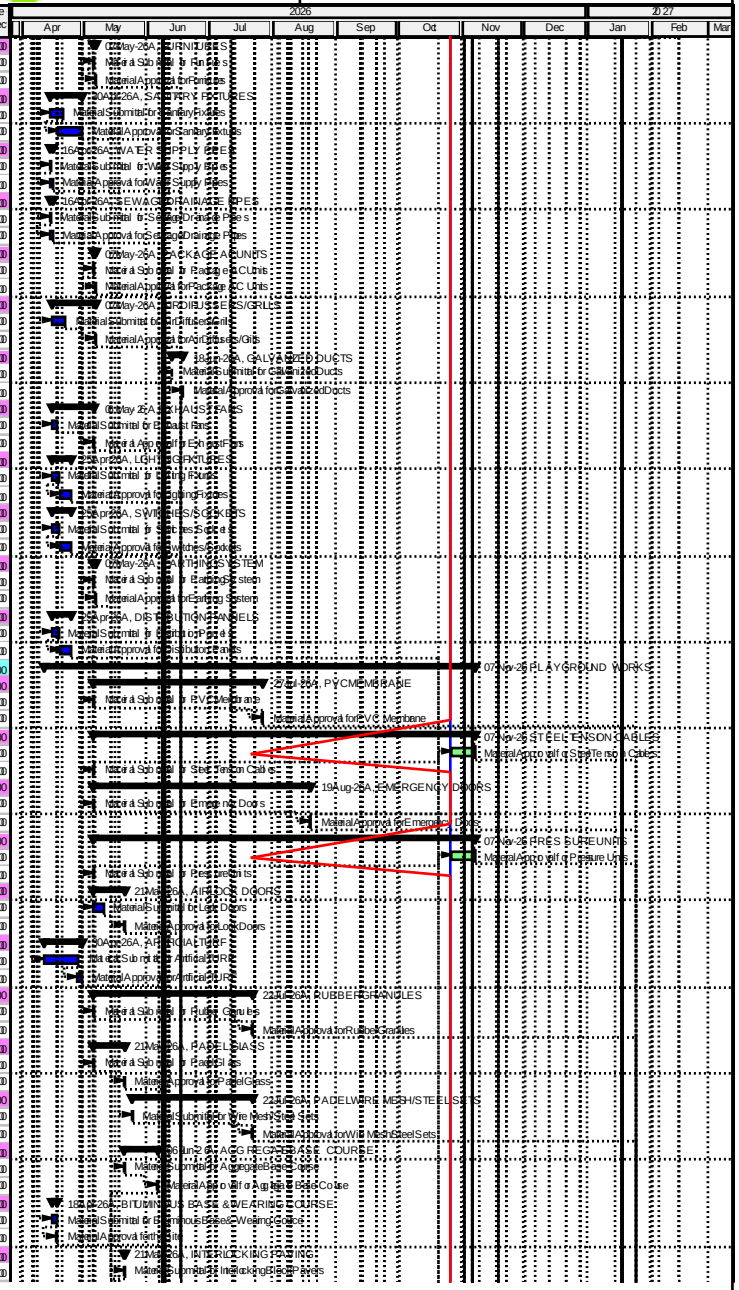


© Oracle Corporation

MLTX-02-004 - Playground Initiative for Western Region (Asir-Jazan -Jeddah)

Updateded schedule D.D 26-10-2026

ActivityID	ActivityName	Orginal Duration	Schedule %	Performance% Complete	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Variance - BL Project
MLTX02-004EN-133	Material Approval for Interlocking Block Pavers	1.00	100%	100%	21-May-26	21-May-26	21 May-26 A	21-May-26A	$000	$000	$0.00	0.00
MARKING PAINT		6.00	0%	0%	13-Apr-26	19-Apr-26	13-Apr-26 A	19-Apr-26A	$000	$000	$0.00	0.00
MLTX02-004EN-136	Material Submittal for Making Paint	5.00	100%	100%	13-Apr-26	18-Apr-26	13-Apr-26 A	18-Apr-26A	$000	$000	$0.00	0.00
MLTX02-004EN-140	Material Approval for Marking Paint	2.00	100%	100%	18-Apr-26	19-Apr-26	18-Apr-26 A	19-Apr-26A	$000	$000	$0.00	0.00
PACKAGE ACUNITS		1.00	0%	0%	21-May-26	21-May-26	21 May-26 A	21-May-26A	$000	$000	$0.00	0.00
MLTX02-004EN-137	Material Submittal for Package ACUnits	1.00	100%	100%	21-May-26	21-May-26	21 May-26 A	21-May-26A	$000	$000	$0.00	0.00
MLTX02-004EN-137	Material Approval for Package AC Units	1.00	100%	100%	21-May-26	21-May-26	21 May-26 A	21-May-26A	$000	$000	$0.00	0.00
AIRDFUSSERS/GRILLS		2100	0%	0%	13-Apr-26	06-May-26	13-Apr-26 A	06-May-26A	$000	$000	$0.00	0.00
MLTX02-004EN-137	Material Submittal for AirDifussers/Grills	9.00	100%	100%	13-Apr-26	22-Apr-26	13-Apr-26 A	22-Apr-26A	$000	$000	$0.00	0.00
MLTX02-004EN-137	Material Approval for AirDifussers/Grills	1.00	100%	100%	06-May-26	06-May-26	06-May-26 A	06-May-26A	$000	$000	$0.00	0.00
GALVANIZEDUCTS		6.00	0%	0%	13-Jun-26	18-Jun-26	13-Jun-26 A	18-Jun-26A	$000	$000	$0.00	0.00
MLTX02-004EN-137	Material Submittal for GalvanizedDuct	1.00	100%	100%	13-Jun-26	13-Jun-26	13-Jun-26 A	13-Jun-26A	$000	$000	$0.00	0.00
MLTX02-004EN-138	Material Approval for GalvanizedDuct	1.00	100%	100%	18-Jun-26	18-Jun-26	18-Jun-26 A	18-Jun-26A	$000	$000	$0.00	0.00
EXHAUSTFANS		2100	0%	0%	13-Apr-26	06-May-26	13-Apr-26 A	06-May-26A	$000	$000	$0.00	0.00
MLTX02-004EN-138	Material Submittal for Exhaust Fans	5.00	100%	100%	13-Apr-26	18-Apr-26	13-Apr-26 A	18-Apr-26A	$000	$000	$0.00	0.00
MLTX02-004EN-138	Material Approval for Exhaust Fans	1.00	100%	100%	06-May-26	06-May-26	06-May-26 A	06-May-26A	$000	$000	$0.00	0.00
DISTRBUTION BOARDS		9.00	0%	0%	13-Apr-26	22-Apr-26	13-Apr-26 A	22-Apr-26A	$000	$000	$0.00	0.00
MLTX02-004EN-138	Material Submittal for DistributionBoards	3.00	100%	100%	13-Apr-26	15-Apr-26	13-Apr-26 A	15-Apr-26A	$000	$000	$0.00	0.00
MLTX02-004EN-138	Material Approval for Distibuton Boards	6.00	100%	100%	16-Apr-26	22-Apr-26	16-Apr-26 A	22-Apr-26A	$000	$000	$0.00	0.00
POWERCABLES		9.00	0%	0%	13-Apr-26	22-Apr-26	13-Apr-26 A	22-Apr-26A	$000	$000	$0.00	0.00
MLTX02-004EN-138	Material Submittal for PowerCables	3.00	100%	100%	13-Apr-26	15-Apr-26	13-Apr-26 A	15-Apr-26A	$000	$000	$0.00	0.00
MLTX02-004EN-138	Material Approval for PowerCables	6.00	100%	100%	16-Apr-26	22-Apr-26	16-Apr-26 A	22-Apr-26A	$000	$000	$0.00	0.00
LIGHTFIXTURES		9.00	0%	0%	13-Apr-26	22-Apr-26	13-Apr-26 A	22-Apr-26A	$000	$000	$0.00	0.00
MLTX02-004EN-138	Material Submittal for Light Fixtures	3.00	100%	100%	13-Apr-26	15-Apr-26	13-Apr-26 A	15-Apr-26A	$000	$000	$0.00	0.00
MLTX02-004EN-138	Material Approval for Light Fixtures	6.00	100%	100%	16-Apr-26	22-Apr-26	16-Apr-26 A	22-Apr-26A	$000	$000	$0.00	0.00
CCTV MATERIALS		9.00	0%	0%	13-Apr-26	22-Apr-26	13-Apr-26 A	22-Apr-26A	$000	$000	$0.00	0.00
MLTX02-004EN-138	Material Submittal for CCTV	3.00	100%	100%	13-Apr-26	15-Apr-26	13-Apr-26 A	15-Apr-26A	$000	$000	$0.00	0.00
MLTX02-004EN-138	Material Approval for CCTV	6.00	100%	100%	16-Apr-26	22-Apr-26	16-Apr-26 A	22-Apr-26A	$000	$000	$0.00	0.00
POWEROUTLETS/SWITCHES		2.00	0%	0%	06-May-26	07-May-26	06-May-26 A	07-May-26A	$000	$000	$0.00	0.00
MLTX02-004EN-138	Material Submittal for PowerOutlets/Switches	1.00	100%	100%	06-May-26	06-May-26	06-May-26 A	06-May-26A	$000	$000	$0.00	0.00
MLTX02-004EN-138	Material Approval for PowerOutlets/Switches	1.00	100%	100%	07-May-26	07-May-26	07-May-26 A	07-May-26A	$000	$000	$0.00	0.00
LANDSCAPE WORKS		4400	0%	0%	13-Apr-26	06-Jun-26	13-Apr-26 A	06-Jun-26A	$000	$000	$0.00	0.00
INTERLOCKNG PAVING		9.00	0%	0%	13-Apr-26	22-Apr-26	13-Apr-26 A	22-Apr-26A	$000	$000	$0.00	0.00
MLTX02-004EN-140	Material Submittal for InterlockingBlockPavers	3.00	100%	100%	13-Apr-26	15-Apr-26	13-Apr-26 A	15-Apr-26A	$000	$000	$0.00	0.00
MLTX02-004EN-140	Material Approval for Interlocking Block Pavers	6.00	100%	100%	16-Apr-26	22-Apr-26	16-Apr-26 A	22-Apr-26A	$000	$000	$0.00	0.00
CURBSTONE		9.00	0%	0%	13-Apr-26	22-Apr-26	13-Apr-26 A	22-Apr-26A	$000	$000	$0.00	0.00
MLTX02-004EN-141	Material Submittal for Curbstone	3.00	100%	100%	13-Apr-26	15-Apr-26	13-Apr-26 A	15-Apr-26A	$000	$000	$0.00	0.00
MLTX02-004EN-141	Material Approval for Curbstone	6.00	100%	100%	16-Apr-26	22-Apr-26	16-Apr-26 A	22-Apr-26A	$000	$000	$0.00	0.00
PAVEMENTMARKNG		6.00	0%	0%	13-Apr-26	19-Apr-26	13-Apr-26 A	19-Apr-26A	$000	$000	$0.00	0.00
MLTX02-004EN-133	Material Submittal for Pavement Makings	5.00	100%	100%	13-Apr-26	18-Apr-26	13-Apr-26 A	18-Apr-26A	$000	$000	$0.00	0.00
MLTX02-004EN-133	Material Approval for Pavement Makings	2.00	100%	100%	18-Apr-26	19-Apr-26	18-Apr-26 A	19-Apr-26A	$000	$000	$0.00	0.00
TRAFFC SIGNS		2400	0%	0%	06-May-26	06-Jun-26	06-May-26 A	06-Jun-26A	$000	$000	$0.00	0.00
MLTX02-004EN-133	Material Submittal for TrafficSigns	1.00	100%	100%	06-May-26	06-May-26	06-May-26 A	06-May-26A	$000	$000	$0.00	0.00
MLTX02-004EN-133	Material Approval for TrafficSigns	1.00	100%	100%	06-Jun-26	06-Jun-26	06-Jun-26 A	06-Jun-26A	$000	$000	$0.00	0.00
IRRGATIONPIPESSPRINKLERS		3400	0%	0%	13-Apr-26	21-May-26	13-Apr-26 A	21-May-26A	$000	$000	$0.00	0.00
MLTX02-004EN-134	Material Submittal for Irrigation Pipes/Sprinkles	5.00	100%	100%	13-Apr-26	18-Apr-26	13-Apr-26 A	18-Apr-26A	$000	$000	$0.00	0.00
MLTX02-004EN-134	Material Approval for Irrigation Pipes/Sprinkles	1.00	100%	100%	21-May-26	21-May-26	21 May-26 A	21-May-26A	$000	$000	$0.00	0.00
AGRICULTURE SOIL		1400	0%	0%	06-May-26	21-May-26	06-May-26 A	21-May-26A	$000	$000	$0.00	0.00
MLTX02-004EN-140	Material Submittal for Agriculture Soil	1.00	100%	100%	06-May-26	06-May-26	06-May-26 A	06-May-26A	$000	$000	$0.00	0.00
MLTX02-004EN-140	Material Approval for Agriculture Soil	1.00	100%	100%	21-May-26	21-May-26	21 May-26 A	21-May-26A	$000	$000	$0.00	0.00
TRACK SURFACE		1400	0%	0%	06-May-26	21-May-26	06-May-26 A	21-May-26A	$000	$000	$0.00	0.00
MLTX02-004EN-140	Material Submittal for Track Suface	1.00	100%	100%	06-May-26	06-May-26	06-May-26 A	06-May-26A	$000	$000	$0.00	0.00
MLTX02-004EN-141	Material Approval for Track Surface	1.00	100%	100%	21-May-26	21-May-26	21 May-26 A	21-May-26A	$000	$000	$0.00	0.00
GRASS/TREES		1400	0%	0%	06-May-26	21-May-26	06-May-26 A	21-May-26A	$000	$000	$0.00	0.00
MLTX02-004EN-141	Material Submittal for Grass/Trees	1.00	100%	100%	06-May-26	06-May-26	06-May-26 A	06-May-26A	$000	$000	$0.00	0.00
MLTX02-004EN-141	Material Approval for Grass/Trees	1.00	100%	100%	21-May-26	21-May-26	21 May-26 A	21-May-26A	$000	$000	$0.00	0.00
CABIES		2.00	0%	0%	06-May-26	07-May-26	06-May-26 A	07-May-26A	$000	$000	$0.00	0.00
MLTX02-004EN-139	Material Submittal for Cables	2.00	100%	100%	06-May-26	07-May-26	06-May-26 A	07-May-26A	$000	$000	$0.00	0.00
MLTX02-004EN-140	Material Approval for Cables	1.00	100%	100%	07-May-26	07-May-26	07-May-26 A	07-May-26A	$000	$000	$0.00	0.00
LIGHTPOLES		2200	0%	0%	13-Apr-26	07-May-26	13-Apr-26 A	07-May-26A	$000	$000	$0.00	0.00
MLTX02-004EN-132	Material Submittal for Lightingpoles	3.00	100%	100%	13-Apr-26	15-Apr-26	13-Apr-26 A	15-Apr-26A	$000	$000	$0.00	0.00
MLTX02-004EN-132	Material Approval for Lightingpoles	1.00	100%	100%	07-May-26	07-May-26	07-May-26 A	07-May-26A	$000	$000	$0.00	0.00
PROCU REMENT		18900	0%	0%	07-May-26	14-Sep-26	20-Apr-26 A	17-Dec-26	$000	$000	$0.00	-9500
SHORTLEAD ITEM		18200	0%	0%	07-May-26	17-Aug-26	20-Apr-26 A	09-Dec-26	$000	$000	$0.00	-112.00
TOILET/SERVICE WORKS		16400	0%	0%	07-May-26	15-Aug-26	07-May-26 A	18-Nov-26	$000	$000	$0.00	-8100
STEELREINFORCEMENT		5800	0%	0%	13-May-26	09-Jul-26	13-May-26 A	18-Jul-26A	$000	$000	$0.00	-700
MLTX02-004PR-11050	PO for Steel Reinforcement	2.00	100%	100%	13-May-26	14-May-26	13-May-26 A	14-May-26A	$000	$000	$0.00	0.00
MLTX02-004PR-11150	Material Delivery of Steel Reinforcement	5.00	100%	100%	05-Jul-26	09-Jul-26	18-Jul-26 A	18-Jul-26A	$000	$000	$0.00	4.00
CONCRETE BLOCKS		7400	0%	0%	07-May-26	13-Jul-26	07-May-26 A	27-Jul-26A	$000	$000	$0.00	-1200
MLTX02-004PR-11230	PO for Concrete Blocks	1.00	100%	100%	07-May-26	07-May-26	07-May-26 A	07-May-26A	$000	$000	$0.00	0.00
MLTX02-004PR-11240	Material Delivery of Concrete Blocks	8.00	100%	100%	05-Jul-26	13-Jul-26	27-Jul-26 A	27-Jul-26A	$000	$000	$0.00	7.00
FLOORWALL TILES		9100	0%	0%	05-Jul-26	15-Aug-26	22-Jul-26 A	27-Sep-26A	$000	$000	$0.00	-2100
MLTX02-004PR-11250	PO for TilingMaterials	5.00	100%	100%	05-Jul-26	09-Jul-26	22-Jul-26 A	22-Jul-26A	$000	$000	$0.00	4.00

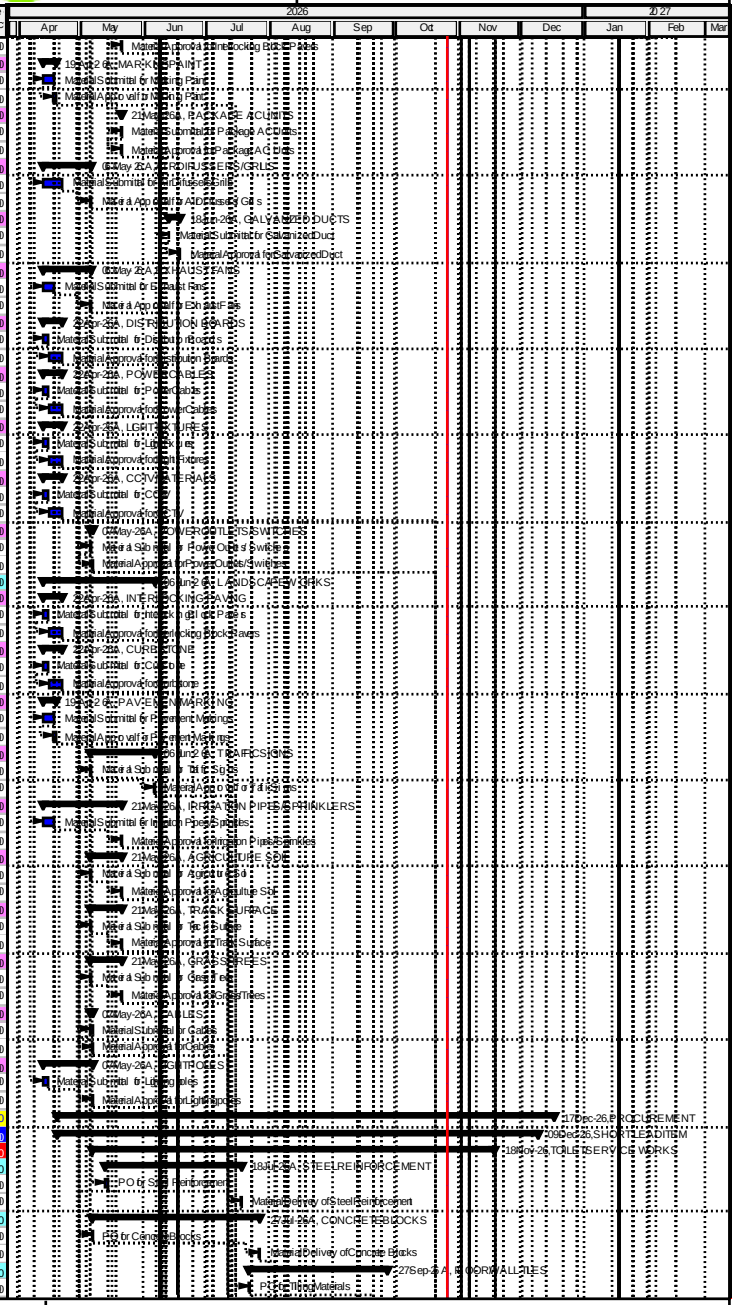


Actual Level of Effort | Remaining Work

Actual Work | Critical Remaining Work

TASK filter: All Activities


© Oracle Corporation

ActivityID	ActivityName	Orginal Duration	Schedule %	Performance% Complete	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Variance - BL Project
MLTX020040PR-11260	Material Delivery of Tailing Material	1300	100%	100%	01-Aug-26	15-Aug-26	27-Sep-25 A	27-Sep-26 A	$000	$000	$0.00	12.00
SUSPENDED CEILING		3700	0%	0%	24-Jun-26	19-Jul-26	24-Jun-26 A	22-Jul-26 A	$000	$000	$0.00	-200
MLTX020040PR-11270	PO for Suspend Ceiling	1.00	100%	100%	24-Jun-26	24-Jun-26	24-Jun-26 A	24-Jun-26 A	$000	$000	$0.00	0.00
MLTX020040PR-11280	Material Delivery of Suspend Ceiling	1300	100%	100%	05-Jul-26	19-Jul-26	22-Jul-26 A	22-Jul-26 A	$000	$000	$0.00	13.00
DOORS/WINDOWS		9900	0%	0%	24-Jun-26	21-Jul-26	24-Jun-26 A	05-Oct-26 A	$000	$000	$0.00	-6400
MLTX020040PR-11290	PO for Doors/Windows	1.00	100%	100%	24-Jun-26	24-Jun-26	24-Jun-26 A	24-Jun-26 A	$000	$000	$0.00	0.00
MLTX020040PR-11300	Material Delivery for Doors/Windows	1500	100%	100%	05-Jul-26	21-Jul-26	01-Oct-26 A	05-Oct-26 A	$000	$000	$0.00	11.00
WATER SUPPLY PIPES		1.00	0%	0%	13-Jun-26	13-Jun-26	13-Jun-26 A	13-Jun-26 A	$000	$000	$0.00	0.00
MLTX020040PR-11330	PO for Water Supply Pipes	1.00	100%	100%	13-Jun-26	13-Jun-26	13-Jun-26 A	13-Jun-26 A	$000	$000	$0.00	0.00
MLTX020040PR-11340	Material Delivery for Water Supply Pipes	1.00	100%	100%	13-Jun-26	13-Jun-26	13-Jun-26 A	13-Jun-26 A	$000	$000	$0.00	0.00
SEWAGE DRAINAGE PIPES		1.00	0%	0%	13-Jun-26	13-Jun-26	13-Jun-26 A	13-Jun-26 A	$000	$000	$0.00	0.00
MLTX020040PR-11350	PO for Sewage/Drainage Pipes	1.00	100%	100%	13-Jun-26	13-Jun-26	13-Jun-26 A	13-Jun-26 A	$000	$000	$0.00	0.00
MLTX020040PR-11360	Material Delivery for Sewage/Drainage Pipes	1.00	100%	100%	13-Jun-26	13-Jun-26	13-Jun-26 A	13-Jun-26 A	$000	$000	$0.00	0.00
SANITARY FIXTURES		11700	0%	0%	16-Jun-26	19-Jul-26	16-Jun-26 A	05-Aug-26 A	$000	$000	$0.00	-1500
MLTX020040PR-11310	PO for Sanitary Fixtures	1.00	100%	100%	16-Jun-26	16-Jun-26	16-Jun-26 A	16-Jun-26 A	$000	$000	$0.00	0.00
MLTX020040PR-11320	Material Delivery for Sanitary Fixtures	1300	100%	100%	05-Jul-26	19-Jul-26	03-Aug-26 A	05-Aug-26 A	$000	$000	$0.00	10.00
PACKAGE A/C UNITS		12800	0%	0%	16-Jun-26	21-Jul-26	16-Jun-26 A	12-Nov-26	$000	$000	$0.00	-9700
MLTX020040PR-11460	Material Delivery for Package A/C Units	1500	100%	0%	05-Jul-26	21-Jul-26	27-Oct-26	12-Nov-26	$000	$000	$0.00	0.00
MLTX020040PR-11450	PO for Package A/C Units	1.00	100%	100%	16-Jun-26	16-Jun-26	16-Jun-26 A	16-Jun-26 A	$000	$000	$0.00	0.00
AIR DIFFUSSERS/ GRILLS		2300	0%	0%	05-Jul-26	30-Jul-26	27-Sep-25 A	27-Sep-26 A	$000	$000	$0.00	22.00
MLTX020040PR-11470	PO for Air Diffusers/Grills	8.00	100%	100%	05-Jul-26	13-Jul-26	27-Sep-25 A	27-Sep-26 A	$000	$000	$0.00	8.00
MLTX020040PR-11480	Material Delivery for Air Diffusers/Grills	1500	100%	100%	14-Jul-26	30-Jul-26	27-Sep-25 A	27-Sep-26 A	$000	$000	$0.00	14.00
GALVANIZED D UCTS		2300	0%	0%	05-Jul-26	30-Jul-26	27-Sep-25 A	27-Sep-26 A	$000	$000	$0.00	22.00
MLTX020040PR-11490	PO for Galvanized Ducts	8.00	100%	100%	05-Jul-26	13-Jul-26	27-Sep-25 A	27-Sep-26 A	$000	$000	$0.00	7.00
MLTX020040PR-11500	Material Delivery for Galvanized Ducts	1500	100%	100%	14-Jul-26	30-Jul-26	27-Sep-25 A	27-Sep-26 A	$000	$000	$0.00	14.00
EXHAUST FANS		9700	0%	0%	18-Jun-26	15-Jul-26	18-Jun-26 A	27-Sep-26 A	$000	$000	$0.00	-6200
MLTX020040PR-11510	PO for Exhaust Fans	1.00	100%	100%	18-Jun-26	18-Jun-26	18-Jun-26 A	18-Jun-26 A	$000	$000	$0.00	0.00
MLTX020040PR-11520	Material Delivery for Exhaust Fans	1000	100%	100%	05-Jul-26	15-Jul-26	27-Sep-25 A	27-Sep-26 A	$000	$000	$0.00	9.00
LIGHTING FIXTURES		11000	0%	0%	01-Jul-26	15-Jul-26	01-Jul-26 A	07-Nov-26	$000	$000	$0.00	-9700
MLTX020040PR-11380	Material Delivery for Lighting Fixtures	1000	100%	0%	05-Jul-26	15-Jul-26	27-Oct-26	07-Nov-26	$000	$000	$0.00	0.00
MLTX020040PR-11370	PO for Lighting Fixtures	2.00	100%	100%	01-Jul-26	02-Jul-26	01-Jul-26 A	02-Jul-26 A	$000	$000	$0.00	0.00
SWITCHES/SOCKETS		10000	0%	0%	24-Jun-26	12-Jul-26	24-Jun-26 A	10-Oct-26 A	$000	$000	$0.00	-7600
MLTX020040PR-11390	PO for Switches/Sockets	1.00	100%	100%	24-Jun-26	24-Jun-26	24-Jun-26 A	24-Jun-26 A	$000	$000	$0.00	0.00
MLTX020040PR-11400	Material Delivery for Switches/Sockets	7.00	100%	100%	05-Jul-26	12-Jul-26	05-Oct-26 A	10-Oct-26 A	$000	$000	$0.00	2.00
EARTHINGSYSTEM		1.00	0%	0%	21-May-26	21-May-26	21-May-26 A	21-May-26 A	$000	$000	$0.00	0.00
MLTX020040PR-11190	PO for EathingSystem	1.00	100%	100%	21-May-26	21-May-26	21-May-26 A	21-May-26 A	$000	$000	$0.00	0.00
MLTX020040PR-11200	Material Delivery for EarthingSystem	1.00	100%	100%	21-May-26	21-May-26	21-May-26 A	21-May-26 A	$000	$000	$0.00	0.00
DISTRIBUTION PANNELS		2000	0%	0%	05-Jul-26	27-Jul-26	27-Oct-26	18-Nov-26	$000	$000	$0.00	0.00
MLTX020040PR-11210	PO for Distribution Panels	5.00	100%	0%	05-Jul-26	09-Jul-26	27-Oct-26	01-Nov-26	$000	$000	$0.00	0.00
MLTX020040PR-11220	Material Delivery for Distibuton Panels	1500	100%	0%	11-Jul-26	27-Jul-26	02-Nov-26	18-Nov-26	$000	$000	$0.00	0.00
FURNITURES		13300	0%	0%	16-Jun-26	27-Jul-26	16-Jun-26 A	18-Nov-26	$000	$000	$0.00	-9700
MLTX020040PR-11420	Material Delivery for Furnitures	2000	100%	0%	05-Jul-26	27-Jul-26	27-Oct-26	18-Nov-26	$000	$000	$0.00	0.00
MLTX020040PR-11410	PO for Furnitures	1.00	100%	100%	16-Jun-26	16-Jun-26	16-Jun-26 A	16-Jun-26 A	$000	$000	$0.00	0.00
PLAYGROUND WORKS		18200	0%	0%	07-May-26	17-Aug-26	20-Apr-26 A	09-Dec-26	$000	$000	$0.00	-112.00
PVC MEMBRANE		13300	0%	0%	16-Jun-26	27-Jul-26	16-Jun-26 A	18-Nov-26	$000	$000	$0.00	-9700
MLTX020040PR-11620	Material Delivery for PVC Membrane	2000	100%	0%	05-Jul-26	27-Jul-26	27-Oct-26	18-Nov-26	$000	$000	$0.00	0.00
MLTX020040PR-11610	PO for PVC Membrane	1.00	100%	100%	16-Jun-26	16-Jun-26	16-Jun-26 A	16-Jun-26 A	$000	$000	$0.00	0.00
ARTIFICIAL TURF		12500	0%	0%	16-Jun-26	18-Jul-26	16-Jun-26 A	09-Nov-26	$000	$000	$0.00	-9700
MLTX020040PR-11860	Material Delivery for Artifical TURF	1200	100%	0%	05-Jul-26	18-Jul-26	27-Oct-26	09-Nov-26	$000	$000	$0.00	0.00
MLTX020040PR-11850	PO for Artifical TURF	1.00	100%	100%	16-Jun-26	16-Jun-26	16-Jun-26 A	16-Jun-26 A	$000	$000	$0.00	0.00
RUBBER GRANULES		12500	0%	0%	16-Jun-26	18-Jul-26	16-Jun-26 A	09-Nov-26	$000	$000	$0.00	-9700
MLTX020040PR-11880	Material Delivery for Rubber Granules	1200	100%	0%	05-Jul-26	18-Jul-26	27-Oct-26	09-Nov-26	$000	$000	$0.00	0.00
MLTX020040PR-11870	PO for Rubber Granules	1.00	100%	100%	16-Jun-26	16-Jun-26	16-Jun-26 A	16-Jun-26 A	$000	$000	$0.00	0.00
PADEL GLASS		13100	0%	0%	16-Jun-26	25-Jul-26	16-Jun-26 A	16-Nov-26	$000	$000	$0.00	-9700
MLTX020040PR-11900	Material Delivery for Padel Glass	1800	100%	0%	05-Jul-26	25-Jul-26	27-Oct-26	16-Nov-26	$000	$000	$0.00	0.00
MLTX020040PR-11890	PO for Padel Glass	1.00	100%	100%	16-Jun-26	16-Jun-26	16-Jun-26 A	16-Jun-26 A	$000	$000	$0.00	0.00
PADEL WIRE MESH/STEEL SETS		12800	0%	0%	16-Jun-26	21-Jul-26	16-Jun-26 A	12-Nov-26	$000	$000	$0.00	-9700
MLTX020040PR-11920	Material Delivery for Wire Mesh/Steel Sets	1500	100%	0%	05-Jul-26	21-Jul-26	27-Oct-26	12-Nov-26	$000	$000	$0.00	0.00
MLTX020040PR-11910	PO for Wire Mesh/Steel Sets	1.00	100%	100%	16-Jun-26	16-Jun-26	16-Jun-26 A	16-Jun-26 A	$000	$000	$0.00	0.00
AGGREGATE BASE COURSE		1.00	0%	0%	21-May-26	21-May-26	21-May-26 A	21-May-26 A	$000	$000	$0.00	0.00
MLTX020040PR-11060	PO for Aggregate Base Course	1.00	100%	100%	21-May-26	21-May-26	21-May-26 A	21-May-26 A	$000	$000	$0.00	0.00
MLTX020040PR-11070	Material Delivery for Aggregate Base Course	1.00	100%	100%	21-May-26	21-May-26	21-May-26 A	21-May-26 A	$000	$000	$0.00	0.00
BITUMINOUS BASE &WEARING COURSE		1500	0%	0%	16-Jun-26	02-Jul-26	16-Jun-26 A	02-Jul-26 A	$000	$000	$0.00	0.00
MLTX020040PR-11080	PO for Bituminous Base & Wearing Course	1.00	100%	100%	16-Jun-26	16-Jun-26	16-Jun-26 A	16-Jun-26 A	$000	$000	$0.00	0.00
MLTX020040PR-11090	Material Delivery for the Site	1.00	100%	100%	02-Jul-26	02-Jul-26	02-Jul-26 A	02-Jul-26 A	$000	$000	$0.00	0.00
INTERLOCKING PAVING		14300	0%	0%	07-May-26	13-Jul-26	20-Apr-26 A	07-May-26 A	$000	$000	$0.00	39.00
MLTX020040PR-11100	PO for Interlocking Block Pavers	1.00	100%	100%	07-May-26	07-May-26	07-May-26 A	07-May-26 A	$000	$000	$0.00	0.00
MLTX020040PR-11110	Material Delivery for Interlocking Block Pavers	8.00	100%	100%	05-Jul-26	13-Jul-26	20-Apr-26 A	20-Apr-26 A	$000	$000	$0.00	7.00
MARKING PAINT		12000	0%	0%	05-Jul-26	17-Aug-26	22-Jul-26 A	09-Dec-26	$000	$000	$0.00	-8200
MLTX020040PR-11440	Material Delivery for Marking Paint	1700	100%	0%	29-Jul-26	17-Aug-26	21-Nov-26	09-Dec-26	$000	$000	$0.00	0.00
MLTX020040PR-11430	PO for Making Paint	1500	100%	100%	05-Jul-26	21-Jul-26	22-Jul-26 A	22-Jul-26 A	$000	$000	$0.00	14.00
PACKAGE A/C UNITS		12800	0%	0%	16-Jun-26	21-Jul-26	16-Jun-26 A	12-Nov-26	$000	$000	$0.00	-9700

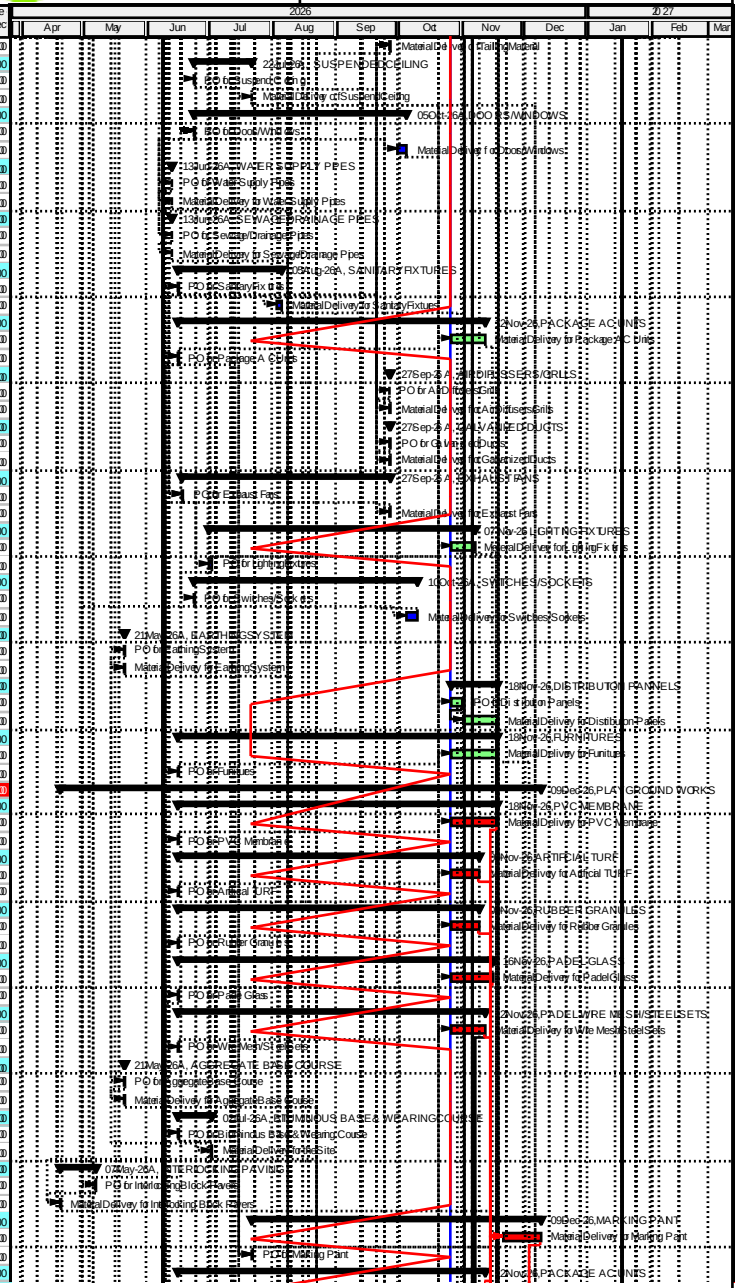


© Oracle Corporation

ActivityID	ActivityName	Orginal Duration	Schedule %	Performance% Complete	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cos	Earned Value Cos	Budgeted Tot Cos	Variance - BL Project
MLTX02.00.4PR-11540	Material Delivery for Package AC Units	1500	100%	0%	05-Jul-26	21-Jul-26	27-Oct-26	12-Nov-26	$000	$000	$0.00	0.00
MLTX02.00.4PR-11530	PO for Package AC Units	1.00	100%	100%	16-Jun-26	16-Jun-26	16-Jun-26A	16-Jun-26A	$000	$000	$0.00	0.00
AIRDIFUSSERS/ GRILLS		11900	0%	0%	16-Jun-26	21-Jul-26	16-Jun-26A	10-Aug-26A	$000	$000	$0.00	-1700
MLTX02.00.4PR-11550	PO for AirDiffussersGrills	1.00	100%	100%	16-Jun-26	16-Jun-26	16-Jun-26A	16-Jun-26A	$000	$000	$0.00	0.00
MLTX02.00.4PR-11560	Material Delivery for AirDiffussers/Grills	1500	100%	100%	05-Jul-26	21-Jul-26	08-Aug-26A	10-Aug-26A	$000	$000	$0.00	12.00
GALVANIZED DUCTS		11900	0%	0%	16-Jun-26	21-Jul-26	16-Jun-26A	12-Aug-26A	$000	$000	$0.00	-1900
MLTX02.00.4PR-11570	PO for GalvanizedDuct	1.00	100%	100%	16-Jun-26	16-Jun-26	16-Jun-26A	16-Jun-26A	$000	$000	$0.00	0.00
MLTX02.00.4PR-11580	Material Delivery for GalvanizedDuct	1500	100%	100%	05-Jul-26	21-Jul-26	08-Aug-26A	12-Aug-26A	$000	$000	$0.00	10.00
EXHAUST FANS		11900	0%	0%	16-Jun-26	21-Jul-26	16-Jun-26A	18-Aug-26A	$000	$000	$0.00	-2400
MLTX02.00.4PR-11590	PO for Exhaust Fans	1.00	100%	100%	16-Jun-26	16-Jun-26	16-Jun-26A	16-Jun-26A	$000	$000	$0.00	0.00
MLTX02.00.4PR-11600	Material Delivery for Exhaust Fans	1500	100%	100%	05-Jul-26	21-Jul-26	17-Aug-26A	18-Aug-26A	$000	$000	$0.00	13.00
DISTRBUTION BOARDS		8200	0%	0%	22-Jul-26	13-Aug-26	22-Jul-26A	12-Nov-26	$000	$000	$0.00	-7700
MLTX02.00.4PR-11720	Material Delivery for Distibuton Boards	1500	100%	0%	28-Jul-26	13-Aug-26	27-Oct-26	12-Nov-26	$000	$000	$0.00	0.00
MLTX02.00.4PR-11710	PO for DistributionBoards	5.00	100%	100%	22-Jul-26	27-Jul-26	22-Jul-26A	22-Jul-26A	$000	$000	$0.00	4.00
POWERCABLES		11500	0%	0%	16-Jun-26	15-Jul-26	16-Jun-26A	16-Sep-26A	$000	$000	$0.00	-5400
MLTX02.00.4PR-11730	PO for PowerCables	1.00	100%	100%	16-Jun-26	16-Jun-26	16-Jun-26A	16-Jun-26A	$000	$000	$0.00	0.00
MLTX02.00.4PR-11740	Material Delivery for PowerCables	1000	100%	100%	05-Jul-26	15-Jul-26	16-Sep-26A	16-Sep-26A	$000	$000	$0.00	9.00
LIGHTFIXTURES		12900	0%	0%	16-Jun-26	22-Jul-26	16-Jun-26A	14-Nov-26	$000	$000	$0.00	-9700
MLTX02.00.4PR-11760	Material Delivery for Light Fixtures	1600	100%	0%	05-Jul-26	22-Jul-26	27-Oct-26	14-Nov-26	$000	$000	$0.00	0.00
MLTX02.00.4PR-11750	PO for Light Fixtures	1.00	100%	100%	16-Jun-26	16-Jun-26	16-Jun-26A	16-Jun-26A	$000	$000	$0.00	0.00
CCTV MATERIALS		2100	0%	0%	05-Jul-26	28-Jul-26	27-Oct-26	19-Nov-26	$000	$000	$0.00	0.00
MLTX02.00.4PR-11770	PO for CCTV	6.00	100%	0%	05-Jul-26	11-Jul-26	27-Oct-26	02-Nov-26	$000	$000	$0.00	0.00
MLTX02.00.4PR-11780	Material Delivery for CCTV	1500	100%	0%	12-Jul-26	28-Jul-26	03-Nov-26	19-Nov-26	$000	$000	$0.00	0.00
POWEROUTLETS/ SWITCHES		1600	0%	0%	05-Jul-26	28-Jul-26	27-Oct-26	14-Nov-26	$000	$000	$0.00	5.00
MLTX02.00.4PR-11790	PO for PowerOutlets/Switches	6.00	100%	0%	05-Jul-26	11-Jul-26	27-Oct-26	02-Nov-26	$000	$000	$0.00	0.00
MLTX02.00.4PR-11800	Material Delivery for PowerOutlets/Switches	6.00	100%	0%	22-Jul-26	28-Jul-26	03-Nov-26	14-Nov-26	$000	$000	$0.00	0.00
LANDSCAPE WORKS		17100	0%	0%	07-May-26	10-Aug-26	20-Apr-26A	26-Nov-26	$000	$000	$0.00	-107.00
INTERLOCKING PAVING		14700	0%	0%	07-May-26	18-Jul-26	20-Apr-26A	27-Oct-26	$000	$000	$0.00	-100.00
MLTX02.00.4PR-11830	PO for InterlockingBlock Pavers	1.00	100%	100%	07-May-26	07-May-26	07-May-26A	07-May-26A	$000	$000	$0.00	0.00
MLTX02.00.4PR-11840	Material Delivery for Interlocking Block Pavers	1200	100%	100%	05-Jul-26	18-Jul-26	20-Apr-26A	27-Oct-26	$000	$000	$0.00	-147.00
CURBSTONE		12700	0%	0%	07-May-26	18-Jul-26	07-May-26A	14-Sep-26A	$000	$000	$0.00	-5000
MLTX02.00.4PR-11970	PO for Curbstone	1.00	100%	100%	07-May-26	07-May-26	07-May-26A	07-May-26A	$000	$000	$0.00	0.00
MLTX02.00.4PR-11980	Material Delivery for Curbstone	1200	100%	100%	05-Jul-26	18-Jul-26	14-Sep-26A	14-Sep-26A	$000	$000	$0.00	11.00
PAVEMENT MARKNG		9600	0%	0%	05-Jul-26	21-Jul-26	18-Jul-26A	07-Nov-26	$000	$000	$0.00	-8100
MLTX02.00.4PR-11130	Material Delivery for Pavement Makings	1000	100%	0%	11-Jul-26	21-Jul-26	27-Oct-26	07-Nov-26	$000	$000	$0.00	0.00
MLTX02.00.4PR-11120	PO for Pavement Makings	5.00	100%	100%	05-Jul-26	09-Jul-26	18-Jul-26A	18-Jul-26A	$000	$000	$0.00	4.00
TRAFFIC SIGNS		9200	0%	0%	05-Jul-26	21-Jul-26	22-Jul-26A	07-Nov-26	$000	$000	$0.00	-7700
MLTX02.00.4PR-11160	Material Delivery for TrafficSigns	1000	100%	0%	11-Jul-26	21-Jul-26	27-Oct-26	07-Nov-26	$000	$000	$0.00	0.00
MLTX02.00.4PR-11140	PO for TrafficSigns	5.00	100%	100%	05-Jul-26	09-Jul-26	22-Jul-26A	27-Jul-26A	$000	$000	$0.00	0.00
IRRGATION PIPESSPRINKLERS		8500	0%	0%	05-Jul-26	19-Jul-26	18-Jul-26A	15-Aug-26A	$000	$000	$0.00	-1200
MLTX02.00.4PR-11170	PO for Irrigation Pipes/Spinkles	5.00	100%	100%	05-Jul-26	09-Jul-26	18-Jul-26A	18-Jul-26A	$000	$000	$0.00	4.00
MLTX02.00.4PR-11180	Material Delivery for Irrigation Pipes/Spinkles	8.00	100%	100%	11-Jul-26	19-Jul-26	13-Aug-26A	15-Aug-26A	$000	$000	$0.00	6.00
AGRICULTURE SOL		9800	0%	0%	05-Jul-26	23-Jul-26	19-Jul-26A	09-Nov-26	$000	$000	$0.00	-8100
MLTX02.00.4PR-11940	Material Delivery for Agriculture Sol	1200	100%	0%	11-Jul-26	23-Jul-26	27-Oct-26	09-Nov-26	$000	$000	$0.00	0.00
MLTX02.00.4PR-11930	PO for Agriculture Sol	5.00	100%	100%	05-Jul-26	09-Jul-26	18-Jul-26A	18-Jul-26A	$000	$000	$0.00	4.00
TRACK SURFACE		11600	0%	0%	24-Jun-26	15-Jul-26	24-Jun-26A	07-Nov-26	$000	$000	$0.00	-9700
MLTX02.00.4PR-11960	Material Delivery for Track Surface	1000	100%	0%	05-Jul-26	15-Jul-26	27-Oct-26	07-Nov-26	$000	$000	$0.00	0.00
MLTX02.00.4PR-11950	PO for Tack Suface	1.00	100%	100%	24-Jun-26	24-Jun-26	24-Jun-26A	24-Jun-26A	$000	$000	$0.00	0.00
GRASS/TREES		11300	0%	0%	11-Jul-26	10-Aug-26	18-Jul-26A	26-Nov-26	$000	$000	$0.00	-8600
MLTX02.00.4PR-12000	Material Delivery for Grass/Trees	1500	100%	0%	25-Jul-26	10-Aug-26	10-Nov-26	26-Nov-26	$000	$000	$0.00	0.00
MLTX02.00.4PR-11990	PO for Grass/Trees	5.00	100%	100%	11-Jul-26	15-Jul-26	18-Jul-26A	18-Jul-26A	$000	$000	$0.00	4.00
CABLES		7000	0%	0%	11-Jul-26	02-Aug-26	18-Jul-26A	17-Sep-26A	$000	$000	$0.00	-3400
MLTX02.00.4PR-11810	PO for Cables	5.00	100%	100%	11-Jul-26	15-Jul-26	18-Jul-26A	18-Jul-26A	$000	$000	$0.00	4.00
MLTX02.00.4PR-11820	Material Delivery for Cables	1500	100%	100%	16-Jul-26	02-Aug-26	17-Sep-26A	17-Sep-26A	$000	$000	$0.00	14.00
LONG LEAD ITEM		15800	0%	0%	16-Jun-26	14-Sep-26	16-Jun-26A	17-Dec-26	$000	$000	$0.00	-8000
PLAYGROUND WORKS		15800	0%	0%	16-Jun-26	25-Aug-26	16-Jun-26A	17-Dec-26	$000	$000	$0.00	-9700
STEELTENSION CABLES		14700	0%	0%	16-Jun-26	18-Aug-26	16-Jun-26A	05-Dec-26	$000	$000	$0.00	-9200
MLTX02.00.4PR-12050	Staging time	7.00	100%	0%	11-Aug-26	18-Aug-26	28-Nov-26	05-Dec-26	$000	$000	$0.00	0.00
MLTX02.00.4PR-11640	Material Delivery for Steel Tension Cables	1500	100%	0%	16-Jul-26	02-Aug-26	09-Nov-26	24-Nov-26	$000	$000	$0.00	0.00
MLTX02.00.4PR-12010	Material FabricationforSteelTension Cables	1000	100%	0%	05-Jul-26	15-Jul-26	27-Oct-26	07-Nov-26	$000	$000	$0.00	0.00
MLTX02.00.4PR-11630	PO for Steel Tension Cables	1.00	100%	100%	16-Jun-26	16-Jun-26	16-Jun-26A	16-Jun-26A	$000	$000	$0.00	0.00
EMERGENCY DOORS		15300	0%	0%	16-Jun-26	19-Aug-26	16-Jun-26A	12-Dec-26	$000	$000	$0.00	-9700
MLTX02.00.4PR-12060	Staging time	5.00	100%	0%	15-Aug-26	19-Aug-26	07-Dec-26	12-Dec-26	$000	$000	$0.00	0.00
MLTX02.00.4PR-11660	Material Delivery for Emergency Doors	2000	100%	0%	22-Jul-26	13-Aug-26	14-Nov-26	06-Dec-26	$000	$000	$0.00	0.00
MLTX02.00.4PR-12020	Material FabricationforEmergency Doos	1500	100%	0%	05-Jul-26	21-Jul-26	27-Oct-26	12-Nov-26	$000	$000	$0.00	0.00
MLTX02.00.4PR-11650	PO for Emegency Doors	1.00	100%	100%	16-Jun-26	16-Jun-26	16-Jun-26A	16-Jun-26A	$000	$000	$0.00	0.00
PRESSURE UNITS		15800	0%	0%	16-Jun-26	25-Aug-26	16-Jun-26A	17-Dec-26	$000	$000	$0.00	-9700
MLTX02.00.4PR-12070	Staging time	5.00	100%	0%	20-Aug-26	25-Aug-26	13-Dec-26	17-Dec-26	$000	$000	$0.00	0.00
MLTX02.00.4PR-11680	Material Delivery for Pressure Units	2000	100%	0%	22-Jul-26	13-Aug-26	14-Nov-26	06-Dec-26	$000	$000	$0.00	0.00
MLTX02.00.4PR-12030	Material FabricationforPressue Units	1500	100%	0%	05-Jul-26	21-Jul-26	27-Oct-26	12-Nov-26	$000	$000	$0.00	0.00
MLTX02.00.4PR-11670	PO for PressureUnits	1.00	100%	100%	16-Jun-26	16-Jun-26	16-Jun-26A	16-Jun-26A	$000	$000	$0.00	0.00
AIRLOCK DOORS		15300	0%	0%	16-Jun-26	19-Aug-26	16-Jun-26A	12-Dec-26	$000	$000	$0.00	-9700

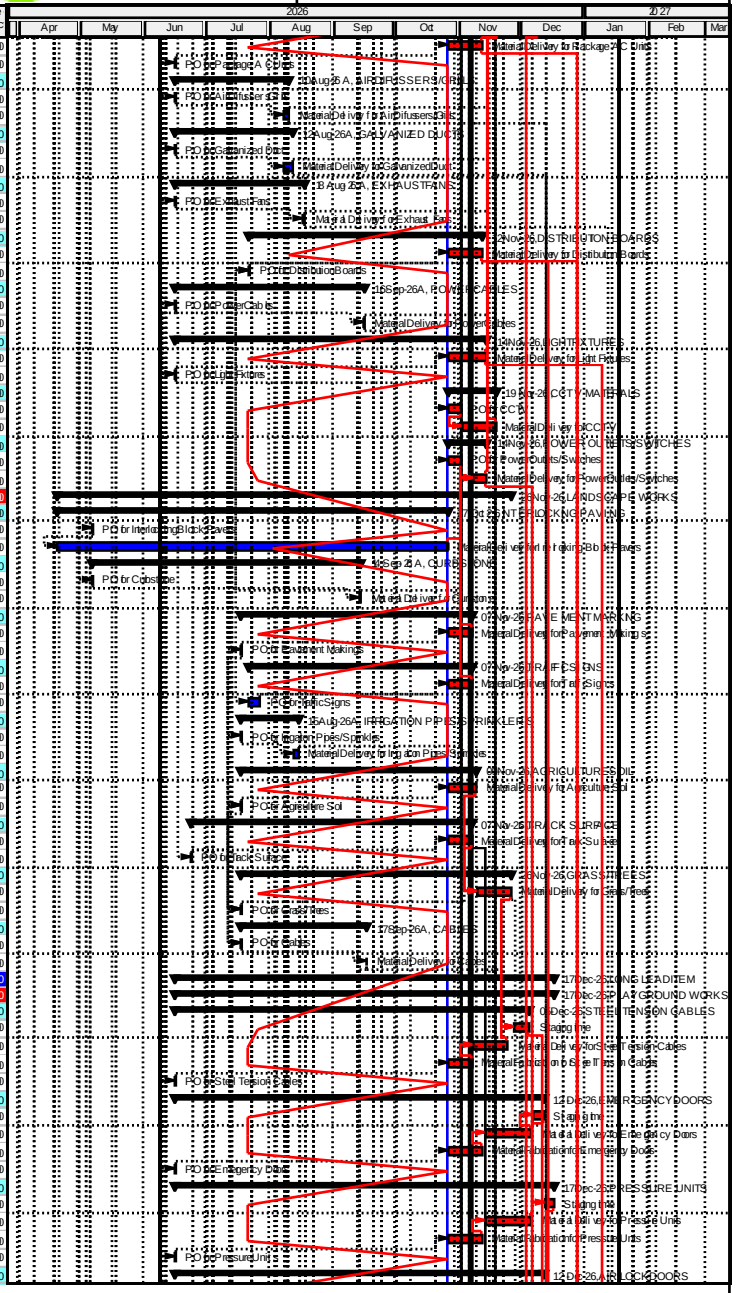


© Oracle Corporation

ActivityID	ActivityName	Orginal Duration	Schedule %	Performance% Complete	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Variance - BL Project
MLTX02-00-MPR-12080	Staging time	5.00	100%	0%	15-Aug-26	19-Aug-26	07-Dec-26	12-Dec-26	$0.00	$0.00	$0.00	0.00
MLTX02-00-MPR-11700	Material Delivery for Lock Doors	2000	100%	0%	22-Jul-26	13-Aug-26	14-Nov-26	06-Dec-26	$0.00	$0.00	$0.00	0.00
MLTX02-00-MPR-12040	Material Fabrication for Lock Doors	1500	100%	0%	05-Jul-26	21-Jul-26	27-Oct-26	12-Nov-26	$0.00	$0.00	$0.00	0.00
MLTX02-00-MPR-11690	PO for Lock Doors	1.00	100%	100%	16-Jun-26	16-Jun-26	16-Jun-26A	16-Jun-26A	$0.00	$0.00	$0.00	0.00
LANDSCAPE WORKS		14900	0%	0%	18-Jun-26	14-Sep-26	18-Jun-26A	28-Sep-26A	$0.00	$0.00	$0.00	-1100
LIGHTPOLES		14900	0%	0%	18-Jun-26	14-Sep-26	18-Jun-26A	28-Sep-26A	$0.00	$0.00	$0.00	-1100
MLTX02-00-MPR-12090	Staging time	5.00	100%	100%	09-Sep-26	14-Sep-26	28-Sep-26A	28-Sep-26A	$0.00	$0.00	$0.00	4.00
MLTX02-00-MPR-11020	PO for Lightingpoles	1.00	100%	100%	18-Jun-26	18-Jun-26	18-Jun-26A	18-Jun-26A	$0.00	$0.00	$0.00	0.00
MLTX02-00-MPR-11030	Material Fabrication for Lighting poles	2500	100%	100%	19-Jul-26	16-Aug-26	27-Aug-26A	27-Aug-26A	$0.00	$0.00	$0.00	24.00
MLTX02-00-MPR-11040	Material Delivery for Lightingpoles	2000	100%	100%	17-Aug-26	08-Sep-26	28-Sep-26A	28-Sep-26A	$0.00	$0.00	$0.00	19.00
CONSTRUCTION PHASE		28600	5436%	4336%	25-Apr-26	25-Jan-27	25-Apr-26A	01-Apr-27	$6814,482.00	$5435,065.36	$12535,459.74	-5300
SITEWORKS		28600	5243%	4269%	25-Apr-26	25-Jan-27	25-Apr-26A	01-Apr-27	$5981,567.59	$4870,274.97	$11408,977.00	-5300
EARTH WORKS		8080	100%	100%	25-Apr-26	30-Jul-26	25-Apr-26A	08-Aug-26A	$1195,736.61	$1195,739.61	$1 195,736.61	-700
MLTX02-004-CN-1310	Excavation(inall types of soil) including Compaction(PlaygroundArea)	1450	100%	100%	25-Apr-26	11-May-26	25-Apr-26A	11-May-26A	$2 119,260.00	$2119,260.00	$2 119,260.00	0.00
MLTX02-004-CN-1320	Excavation(inall types of soil) including Compaction(Service/ToiletBuilding)	1514	100%	100%	27-Apr-26	14-May-26	27-Apr-26A	14-May-26A	$1,077,373.75	$1,077,373.75	$1077,373.75	0.00
MLTX02-004-CN-1330	Excavation(inall types of soil) including Compaction(Landscape Area)	1320	100%	100%	25-Apr-26	10-May-26	25-Apr-26A	10-May-26A	$1,305,541.73	$1,305,541.73	$1 305,541.73	0.00
MLTX02-004-CN-1340	Backfilling onLayers(RockfII) including Compaction(Playground Area)	4350	100%	100%	10-May-26	02-Jul-26	10-May-26A	02-Jul-26A	$2,909,941.90	$2,909,941.90	$2 909,941.90	0.00
MLTX02-004-CN-1350	Backfilling onLayers(RockfII)includingCompacton (ServiceToilet Building)	3900	100%	100%	16-May-26	02-Jul-26	16-May-26A	02-Jul-26A	$51,187.50	$51,187.50	$51,187.50	0.00
MLTX02-004-CN-1360	Backfilling onLayers(RockfII)including Compacton (Landscape Area)	4380	100%	100%	10-May-26	02-Jul-26	10-May-26A	02-Jul-26A	$2,388,750.00	$2,388,750.00	$2,388,750.00	0.00
MLTX02-004-CN-1460	Backfilling onLayers(Selected Soil)including Compaction (ServiceToilet Building)	8.00	100%	100%	05-Jul-26	13-Jul-26	05-Jul-26A	19-Jul-26A	$27,300.00	$27,300.00	$27,300.00	-460
MLTX02-004-CN-1470	Backfilling onLayers(Selected Soil)including Compaction (landscape Area)	1500	100%	100%	14-Jul-26	30-Jul-26	09-Jul-26A	05-Aug-26A	$131,824.88	$131,824.88	$131,824.88	-770
MLTX02-004-CN-1450	Backfilling onLayers(Selected Soil)including Compaction (Playground Area)	1000	100%	100%	14-Jul-26	25-Jul-26	18-Jul-26A	08-Aug-26A	$102,368.85	$102,368.85	$1 023,688.50	-820
LANDSCAPE WORKS		19300	4731%	3604%	05-Jul-26	25-Jan-27	11-Jul-26A	01-Apr-27	$4785,827.58	$3645,286.36	$10115,678.40	-4800
PLAYGROUND AREA		16000	7734%	6432%	05-Jul-26	05-Jan-27	22-Aug-26A	25-Feb-27	$1424,181.20	$1184,436.83	$1,841,387.00	-200
FOOTBALLPLAYGROUND		14800	75%	5208%	05-Jul-26	21-Nov-26	22-Aug-26A	10-Feb-27	$2,588,625.00	$1797,656.68	$3,451,500.00	-2900
MLTX02-004-CN-1330	InstallSportEquipments -Goal /Nets- Football Playground)	1000	0%	0%	10-Nov-26	21-Nov-26	31-Jan-27	10-Feb-27	$0.00	$0.00	$71906.25	0.00
MLTX02-004-CN-1330	Surface Makingand Painting(FoobalPlayground)	1000	0%	0%	27-Oct-26	07-Nov-26	10-Dec-26	21-Dec-26	$0.00	$0.00	$14381.25	0.00
MLTX02-004-CN-1330	Finishingand SurfaceFinish Works (Football Playground)	1500	100%	45%	21-Sep-26	08-Oct-26	12-Oct-26A	12-Nov-26	$1,438,125.00	$646,781.63	$1,438,125.00	-1300
MLTX02-004-CN-1330	Preparation andProofing for Subgade (Football Playground)	1800	100%	100%	05-Jul-26	25-Jul-26	22-Aug-26A	24-Aug-26A	$557,250.00	$557,250.00	$557,250.00	15.00
MLTX02-004-CN-1330	Backfilling andCompacton ofBaseLayers(FoobalPlayground)	1100	100%	100%	26-Jul-26	06-Aug-26	29-Aug-26A	15-Sep-26A	$557,250.00	$557,250.00	$557,250.00	-500
PADEL PLAYGROUND		13000	80%	6625%	26-Jul-26	21-Nov-26	22-Aug-26A	10-Feb-27	$1,716,000.00	$142106.25	$2,145,000.00	-4700
MLTX02-004-CN-1330	InstallSportEquipments -Goal /Nets- Padel Playground)	1000	0%	0%	10-Nov-26	21-Nov-26	31-Jan-27	10-Feb-27	$0.00	$0.00	$32175.00	0.00
MLTX02-004-CN-1330	Surface Makingand Painting(PadelPlayground)	1000	0%	0%	10-Nov-26	21-Nov-26	31-Jan-27	10-Feb-27	$0.00	$0.00	$10725.00	0.00
MLTX02-004-CN-1330	Finishingand SurfaceFinish Works (Padel Playground)	1500	100%	45%	21-Sep-26	08-Oct-26	20-Oct-26A	05-Dec-26	$552,500.00	$248,625.00	$553625.00	-2500
MLTX02-004-CN-1330	Preparation andProofing for Subgade (PadelPlayground)	1100	100%	100%	26-Jul-26	06-Aug-26	22-Aug-26A	24-Aug-26A	$750,750.00	$750,750.00	$750,750.00	8.00
MLTX02-004-CN-1330	Backfilling andCompacton ofBaseLayers(PadelPlayground)	1000	100%	100%	08-Aug-26	18-Aug-26	29-Aug-26A	15-Sep-26A	$429,000.00	$429,000.00	$429,000.00	-600
BASKETBALLPLAYGROUND		13100	70%	425%	08-Aug-26	05-Dec-26	22-Aug-26A	25-Feb-27	$2,184,000.00	$132600.00	$3,120,000.00	-5800
MLTX02-004-CN-1330	InstallSportEquipments -Goal /Nets- Basketball Playground)	1000	0%	0%	22-Nov-26	02-Dec-26	11-Feb-27	23-Feb-27	$0.00	$0.00	$78000.00	0.00
MLTX02-004-CN-1330	Surface Makingand Painting(BasketballPlayground)	1200	0%	0%	22-Nov-26	05-Dec-26	11-Feb-27	25-Feb-27	$0.00	$0.00	$15600.00	0.00
MLTX02-004-CN-1330	Finishingand SurfaceFinish Works (Basketball Playground)	1500	100%	45%	10-Oct-26	26-Oct-26	20-Oct-26A	05-Dec-26	$1,560,000.00	$702,000.00	$1,560,000.00	-2500
MLTX02-004-CN-1330	Preparation andProofing for Subgade (Basketball Playground)	1000	100%	100%	08-Aug-26	18-Aug-26	22-Aug-26A	24-Aug-26A	$312,000.00	$312,000.00	$312,000.00	7.00
MLTX02-004-CN-1330	Backfilling andCompacton ofBaseLayers(BasketballPlayground)	1000	100%	100%	19-Aug-26	30-Aug-26	29-Aug-26A	15-Sep-26A	$312,000.00	$312,000.00	$312,000.00	-600
PADELFENCE		10800	0%	35%	06-Dec-26	05-Jan-27	15-Sep-26A	25-Nov-26	$0.00	$2,900.625	$82875.00	-3400
MLTX02-004-CN-1330	Tempered Glass Fenc Installaton and Fixation	1000	0%	0%	13-Dec-26	23-Dec-26	27-Oct-26	07-Nov-26	$0.00	$0.00	$33150.00	0.00
MLTX02-004-CN-1330	Chain LinkFenceInstallation andFixation	1000	0%	0%	13-Dec-26	23-Dec-26	14-Nov-26	24-Nov-26	$0.00	$0.00	$16575.00	0.00
MLTX02-004-CN-1370	Install of Fence Gates	1100	0%	0%	24-Dec-26	05-Jan-27	14-Nov-26	25-Nov-26	$0.00	$0.00	$4,143.75	0.00
MLTX02-004-CN-1390	ExcavationforFence	5.00	0%	100%	06-Dec-26	10-Dec-26	15-Sep-26A	15-Sep-26A	$0.00	$8287.50	$8,287.50	4.00
MLTX02-004-CN-1390	Concrete Foundation for Fence includingPostsFixation	4.00	0%	100%	06-Dec-26	09-Dec-26	29-Sep-26A	29-Sep-26A	$0.00	$1,657.50	$16575.00	3.00
MLTX02-004-CN-1390	Backfilling andReinstatementforConcrete Foundation	2.00	0%	100%	10-Dec-26	12-Dec-26	04-Oct-26A	06-Oct-26A	$0.00	$4143.75	$4,143.75	-100
CURBSTONE/INTERLOCK		3700	8742%	7904%	29-Sep-26	05-Nov-26	20-Sep-26A	12-Nov-26	$7,753,187.70	$7009,587.70	$8,868,937.70	-1300
MLTX02-004-CN-1330	Interlock Installaton (Grey Scale)forLandScape(IncludingFinishingWorks)	1500	40%	0%	20-Oct-26	05-Nov-26	27-Oct-26	12-Nov-26	$7,486.00	$0.00	$1,859.00	0.00
MLTX02-004-CN-1340	Concrete WorksUnder Curbstone	8.00	100%	100%	29-Sep-26	07-Oct-26	20-Sep-26A	22-Sep-26A	$2,581,585.55	$2581585.55	$2,581,585.55	6.00
MLTX02-004-CN-1340	CurbstoneInstallation	1000	100%	100%	08-Oct-26	19-Oct-26	20-Sep-26A	29-Sep-26A	$1,428,000.15	$442800.15	$4,428,000.15	3.00
AIRDOME		17900	5744%	225%	31-Aug-26	04-Jan-27	11-Jul-26A	16-Mar-27	$3220,000.00	$1261,406.25	$5,606,250.00	-101.00
CIVIL WORKS		10800	100%	50%	31-Aug-26	05-Oct-26	11-Jul-26A	19-Dec-26	$2354,625.00	$1177,312.50	$2,354,625.00	-108.00
MLTX02-004-CN-1370	Install of Membrane CoveringSystem (AirDome)	1200	100%	0%	21-Sep-26	05-Oct-26	06-Dec-26	19-Dec-26	$5,606,250.00	$0.00	$5,606,250.00	0.00
MLTX02-004-CN-1370	Thermal Insulation Works (Air Dome)	6.00	100%	0%	21-Sep-26	28-Sep-26	13-Dec-26	19-Dec-26	$5,606,250.00	$0.00	$5,606,250.00	0.00
MLTX02-004-CN-1370	Cable System Installaton (Air Dome)	8.00	100%	90%	12-Sep-26	20-Sep-26	21-Sep-26A	05-Dec-26	$5,606,250.00	$5045625.00	$5,606,250.00	-5400
MLTX02-004-CN-1370	ExcavationforFoundaton & Playgound Area (Air Dome)	5.00	100%	100%	31-Aug-26	05-Sep-26	11-Jul-26A	12-Aug-26A	$2,803,125.00	$2803125.00	$2,803,125.00	-2400
MLTX02-004-CN-1370	Concrete Worksfor Foundations including Anchor Bolts (Air Dome)	5.00	100%	100%	06-Sep-26	10-Sep-26	29-Jul-26A	22-Sep-26A	$3,924,375.00	$3924375.00	$3,924,375.00	-4300
MECHANICALWORKS		3600	5885%	0%	29-Sep-26	09-Nov-26	20-Dec-26	30-Jan-27	$6,581,125.00	$0.00	$1,121,250.00	0.00
MLTX02-004-CN-1370	AirDuctsand GillsInstallation (Air Dome)	1300	100%	0%	29-Sep-26	13-Oct-26	20-Dec-26	03-Jan-27	$2,803,125.00	$0.00	$2,803,125.00	0.00
MLTX02-004-CN-1370	AirUnitsInstallaton (Air Dome)	1300	8462%	0%	14-Oct-26	28-Oct-26	04-Jan-27	18-Jan-27	$3,785,000.00	$0.00	$4,485,000.00	0.00
MLTX02-004-CN-1370	Exhaust Fans andDucts Instalation (Air Dome)	1000	0%	0%	29-Oct-26	09-Nov-26	19-Jan-27	30-Jan-27	$0.00	$0.00	$3,924,375.00	0.00
ELECTRICAL WORKS		5900	1222%	5%	14-Oct-26	04-Jan-27	15-Oct-26A	04-Mar-27	$2,056,625.00	$84093.75	$1,681,875.00	-4900
MLTX02-004-CN-1370	Distibuton Board and ElectricalWorks (Air Dome)	1500	0%	0%	07-Nov-26	23-Nov-26	04-Jan-27	20-Jan-27	$0.00	$0.00	$2,803,125.00	0.00
MLTX02-004-CN-1370	External ElectricalConnection Works (Air Dome)	1500	0%	0%	24-Nov-26	10-Dec-26	21-Jan-27	07-Feb-27	$0.00	$0.00	$2,803,125.00	0.00
MLTX02-004-CN-1370	Emergency GeneratorInstallation (AirDome)	1100	0%	0%	12-Dec-26	23-Dec-26	08-Feb-27	20-Feb-27	$0.00	$0.00	$5,606,250.00	0.00
MLTX02-004-CN-1370	Contol System Installation(AirDome)	1000	0%	0%	24-Dec-26	04-Jan-27	21-Feb-27	04-Mar-27	$0.00	$0.00	$2,803,125.00	0.00
MLTX02-004-CN-1370	Light FixtureWorks(AirDome)	1500	7333%	30%	14-Oct-26	31-Oct-26	15-Oct-26A	03-Jan-27	$2,056,625.00	$84093.75	$2,803,125.00	-5400
FINISHES WORKS		4300	0%	0%	24-Nov-26	26-Dec-26	21-Jan-27	16-Mar-27	$0.00	$0.00	$4,485,000.00	-1500

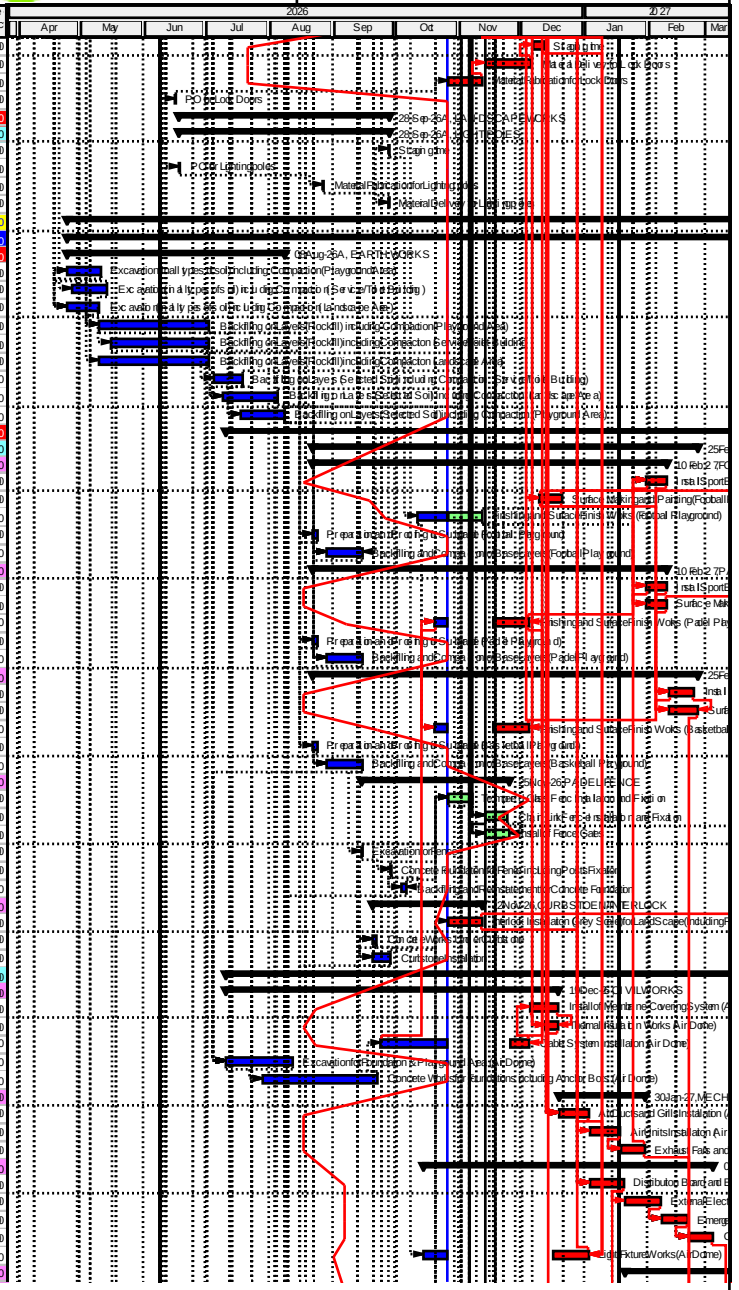


© Oracle Corporation

ActivityID	ActivityName	Orginal Duration	Schedule %	Performance% Complete	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Variance - BL Project
MLTX02-004CN-137	Doors Installation Including Emegency,Entrance doors (Air Dome)	1500	0%	0%	24-Nov-26	10-Dec-26	21-Jan-27	07-Feb-27	$000	$000	$2,212,500.00	0.00
MLTX02-004CN-137	Logoand Signs Installation(AirDome)	1300	0%	0%	12-Dec-26	26-Dec-26	27-Feb-27	16-Mar-27	$000	$000	$2,212,500.00	0.00
IRRIGATION NETWORK		2900	1509%	7929%	20-Oct-26	21-Nov-26	22-Aug-26A	07-Dec-26	$4,089,750	$212,225.00	$2,676,700.00	-6400
MLTX02-004CN-14650	Installing ofBubblers andSprayers	3.00	0%	0%	18-Nov-26	21-Nov-26	05-Dec-26	07-Dec-26	$000	$000	$46,150.00	0.00
MLTX02-004CN-14640	Installing ofValvesand ftings for IrigationNetwork	3.00	0%	80%	09-Nov-26	11-Nov-26	15-Sep-26A	28-Nov-26	$000	$2,738.00	$46,475.00	-6000
MLTX02-004CN-14620	Installing ofHDPE Pipes forIrigation Network (Main Line)	1200	50%	100%	20-Oct-26	02-Nov-26	22-Aug-26A	31-Aug-26A	$4,089,750	$80,795.00	$80,795.00	3.00
MLTX02-004CN-14630	Installing ofHDPE Pipes forIrigation Network (BranchLines)	5.00	0%	100%	03-Nov-26	08-Nov-26	31-Aug-26A	31-Aug-26A	$000	$9,425.00	$94,250.00	4.00
NATURALGROUND		5.00	0%	0%	12-Nov-26	17-Nov-26	29-Nov-26	03-Dec-26	$000	$000	$1,170.00	0.00
MLTX02-004CN-13420	Compacted NaturalGroundSoilInstallation Works for Landscape	5.00	0%	0%	12-Nov-26	17-Nov-26	29-Nov-26	03-Dec-26	$000	$000	$1,170.00	0.00
PLANTING		1200	0%	8.33%	22-Nov-26	12-Dec-26	12-Oct-26A	20-Dec-26	$000	$7,357.35	$8,846.35	-4200
MLTX02-004CN-13480	Placement of SweetAgricultural Soil (Including Levelling andGrading)	5.00	0%	0%	22-Nov-26	26-Nov-26	08-Dec-26	13-Dec-26	$000	$000	$3,219.45	0.00
MLTX02-004CN-13500	Placement and Fixationof Trees	6.00	0%	0%	28-Nov-26	03-Dec-26	14-Dec-26	20-Dec-26	$000	$000	$3,875.25	0.00
MLTX02-004CN-13490	Placement of LawnGroundCover(Rolling and Compacton)	7.00	0%	42%	05-Dec-26	12-Dec-26	12-Oct-26A	03-Nov-26	$000	$7,357.35	$1,751.75	-1300
WALKING/BIKE PATHS		8.00	0%	50%	13-Dec-26	21-Dec-26	16-Aug-26A	07-Nov-26	$000	$276,412.50	$5,528,250.00	-6300
MLTX02-004CN-13430	BikePathPreparationand InstallationWorks	8.00	0%	50%	13-Dec-26	21-Dec-26	16-Aug-26A	07-Nov-26	$000	$142,045.32	$2,840,906.63	-6300
MLTX02-004CN-13440	WalkingPath Preparaton and InstallationWorks	8.00	0%	50%	13-Dec-26	21-Dec-26	16-Aug-26A	04-Nov-26	$000	$134,367.19	$2,687,343.38	-6100
GENERAL/FURNITURE		12100	1197%	7533%	20-Oct-26	25-Jan-27	19-Sep-26A	01-Apr-27	$1,012,488.88	$637,231.28	$8,459,515.95	-7900
MLTX02-004CN-13400	Stamped Concete Worksfor landScape(IncludingFinishingWorks)	7.00	0%	0%	22-Dec-26	29-Dec-26	20-Mar-27	27-Mar-27	$000	$000	$28,080.00	0.00
MLTX02-004CN-13470	TrafficSignsPosts and Poles Installation	5.00	0%	0%	13-Jan-27	18-Jan-27	28-Mar-27	01-Apr-27	$000	$000	$9,750.00	0.00
MLTX02-004CN-13870	Fixationand Installationof Steel Frame for Benches	1000	0%	0%	22-Dec-26	02-Jan-27	08-Nov-26	18-Nov-26	$000	$000	$17,276.00	0.00
MLTX02-004CN-13880	Fixationand Installationof Benches	9.00	0%	0%	03-Jan-27	12-Jan-27	19-Nov-26	29-Nov-26	$000	$000	$40,310.73	0.00
MLTX02-004CN-13890	Fixationand Installationof PecastConcrete Seats (Rectangular)	9.00	0%	0%	03-Jan-27	12-Jan-27	19-Nov-26	29-Nov-26	$000	$000	$43,680.00	0.00
MLTX02-004CN-13900	Fixationand Installationof PecastConcrete Seats (Circula)	9.00	0%	0%	03-Jan-27	12-Jan-27	19-Nov-26	29-Nov-26	$000	$000	$17,160.00	0.00
MLTX02-004CN-13910	Fixationand Installationof PecastConcrete Trash Bins	1100	0%	0%	13-Jan-27	25-Jan-27	21-Dec-26	02-Jan-27	$000	$000	$14,625.00	0.00
MLTX02-004CN-14360	Installing ofSiteLightPoles	1200	0%	92%	30-Dec-26	12-Jan-27	04-Oct-26A	27-Mar-27	$000	$434,733.52	$4,725,363.45	-1340
MLTX02-004CN-14350	Preliminary Works forSiteLightPoles IncludingCableand Bases Works	1200	50%	100%	20-Oct-26	02-Nov-26	19-Sep-26A	01-Oct-26A	$1,012,488.88	$202,497.75	$2,024,977.75	1.00
PARKING		7500	0%	30%	30-Dec-26	12-Jan-27	11-Aug-26A	04-Nov-26	$000	$2,925.00	$97,499.00	-6100
MLTX02-004CN-13370	Interlock Installaton (8 Cm)for ParkingArea(IncludingFinishing Works)	8.00	0%	0%	04-Jan-27	12-Jan-27	27-Oct-26	04-Nov-26	$000	$000	$68,249.00	0.00
MLTX02-004CN-13380	Site Preparation & CompactionUnderInterlockfor ParkingArea	4.00	0%	100%	30-Dec-26	03-Jan-27	11-Aug-26A	18-Oct-26A	$000	$2,925.00	$29,250.00	-5400
TOILET/SERVICE BULDING		12600	7394%	5013%	14-Jul-26	30-Nov-26	19-Jul-26A	06-Dec-26	$8,339,148.88	$564,790.39	$1,126,547.11	-100
STRUCTUREWORKS		3700	100%	100%	14-Jul-26	14-Sep-26	19-Jul-26A	11-Aug-26A	$1,579,500.00	$157,950.00	$1,579,500.00	33.00
CONCRETE WORKS		3700	100%	100%	15-Jul-26	14-Sep-26	19-Jul-26A	03-Aug-26A	$1,137,825.00	$113,782.50	$1,137,825.00	39.00
SUB-STRUCTURE		500	100%	100%	15-Jul-26	23-Jul-26	19-Jul-26A	25-Jul-26A	$33,345.00	$33,345.00	$33,345.00	2.00
MLTX02-004CN-135	Plain Concete Under Footing	3.00	100%	100%	15-Jul-26	18-Jul-26	19-Jul-26A	19-Jul-26A	$1,170.00	$1,170.00	$1,170.00	2.00
MLTX02-004CN-135	ReinforcedConcrete Works for SlabonGrade including Steel Fixing	5.00	100%	100%	19-Jul-26	23-Jul-26	20-Jul-26A	25-Jul-26A	$32,175.00	$32,175.00	$32,175.00	0.00
SUPER-STRUCTURE		2400	100%	100%	29-Jul-26	14-Sep-26	30-Jul-26A	03-Aug-26A	$80,437.50	$80,437.50	$80,437.50	37.00
MLTX02-004CN-135	AAC Panels Works for Walls	1800	100%	100%	29-Jul-26	18-Aug-26	30-Jul-26A	01-Aug-26A	$48,262.50	$48,262.50	$48,262.50	16.00
MLTX02-004CN-135	Parpet Works and Lintels	800	100%	100%	06-Sep-26	14-Sep-26	01-Aug-26A	02-Aug-26A	$16,087.50	$16,087.50	$16,087.50	6.00
MLTX02-004CN-135	AAC Panels Works for Slabs	1500	100%	100%	19-Aug-26	05-Sep-26	02-Aug-26A	03-Aug-26A	$16,087.50	$16,087.50	$16,087.50	13.00
UNDER GROUNDSEPTIC TANK		1100	100%	100%	15-Jul-26	12-Aug-26	23-Jul-26A	27-Jul-26A	$33,930.00	$33,930.00	$33,930.00	21.00
MLTX02-004CN-14510	Plain Concete Under Footing	3.00	100%	100%	15-Jul-26	18-Jul-26	23-Jul-26A	23-Jul-26A	$1,170.00	$1,170.00	$1,170.00	2.00
MLTX02-004CN-14520	ReinforcedConcrete Works for Tank SlabIncludingShutteing and Steel Fixing	8.00	100%	100%	04-Aug-26	12-Aug-26	27-Jul-26A	27-Jul-26A	$8,775.00	$8,775.00	$8,775.00	7.00
MLTX02-004CN-14530	ReinforcedConcrete Works for Tank FountationIncludingShutteing and Steel Fixing	8.00	100%	100%	19-Jul-26	27-Jul-26	23-Jul-26A	23-Jul-26A	$7,605.00	$7,605.00	$7,605.00	7.00
MLTX02-004CN-14540	ReinforcedConcrete Works for Tank Walls including Steel Fixing	6.00	100%	100%	28-Jul-26	03-Aug-26	27-Jul-26A	27-Jul-26A	$16,380.00	$16,380.00	$16,380.00	5.00
THERMAL& MOISTER PROTECTION		2800	100%	100%	14-Jul-26	27-Aug-26	20-Jul-26A	11-Aug-26A	$10,237.50	$10,237.50	$10,237.50	19.00
ANTI TERMITCONTROL		1000	100%	100%	14-Jul-26	14-Jul-26	20-Jul-26A	30-Jul-26A	$4,387.50	$4,387.50	$4,387.50	-900
MLTX02-004CN-135	AntiTermite Works Under Faundation	1.00	100%	100%	14-Jul-26	14-Jul-26	20-Jul-26A	20-Jul-26A	$1,755.00	$1,755.00	$1,755.00	0.00
MLTX02-004CN-140	AntiTermite Works Under Slab onGradeand Gratle Beams	1.00	100%	100%	14-Jul-26	14-Jul-26	30-Jul-26A	30-Jul-26A	$2,632.50	$2,632.50	$2,632.50	0.00
POLYETHYLENESHEET		1000	100%	100%	14-Jul-26	14-Jul-26	20-Jul-26A	30-Jul-26A	$2,193.75	$2,193.75	$2,193.75	-900
MLTX02-004CN-135	Water ProofingUnderBlinding Concrete(PolyhelenSheet)	1.00	100%	100%	14-Jul-26	14-Jul-26	20-Jul-26A	20-Jul-26A	$87.50	$87.50	$87.75	0.00
MLTX02-004CN-135	Water ProofingUnderSlab on Grade (Polythelen Sheet)	1.00	100%	100%	14-Jul-26	14-Jul-26	30-Jul-26A	30-Jul-26A	$1,316.25	$1,316.25	$1,316.25	0.00
EPOXY		1000	100%	100%	13-Aug-26	27-Aug-26	09-Aug-26A	11-Aug-26A	$3,656.25	$3,656.25	$3,656.25	10.00
MLTX02-004CN-140	Surface Preparaton for Epoxy Coating	5.00	100%	100%	13-Aug-26	18-Aug-26	09-Aug-26A	09-Aug-26A	$1,096.88	$1,096.88	$1,096.88	4.00
MLTX02-004CN-140	EpoxyCoating forWalls and Slabof Tank	8.00	100%	100%	19-Aug-26	27-Aug-26	11-Aug-26A	11-Aug-26A	$2,559.38	$2,559.38	$2,559.38	7.00
MASONARY WORK		400	100%	100%	25-Jul-26	28-Jul-26	10-Aug-26A	12-Aug-26A	$1,228.50	$1,228.50	$12285.00	1.00
MLTX02-004CN-14080	CMU MasonaryWorksIncluding all Accessories	4.00	100%	100%	25-Jul-26	28-Jul-26	10-Aug-26A	12-Aug-26A	$1,228.50	$1,228.50	$12285.00	1.00
THERMAL& MOISTER PROTECTION		2600	100%	100%	15-Sep-26	08-Oct-26	15-Sep-26A	11-Oct-26A	$34,700.25	$2,470.025	$34700.25	-200
MLTX02-004CN-14050	PreparingSurface andPreliminaryWorksforToilets Waterpoofing	4.00	100%	100%	15-Sep-26	19-Sep-26	15-Sep-26A	15-Sep-26A	$2,106.00	$2,106.00	$2,106.00	3.00
MLTX02-004CN-14060	FinalizeWaterProofing Worksfor Toilets	5.00	100%	100%	20-Sep-26	26-Sep-26	15-Sep-26A	28-Sep-26A	$4,914.00	$4,914.00	$4,914.00	-600
MLTX02-004CN-14070	PreparingSurface andPreliminaryWorksforRoofing andWet Areas Insulaton	5.00	100%	100%	27-Sep-26	01-Oct-26	27-Sep-26A	27-Sep-26A	$11,072.10	$1,107.210	$11,072.10	4.00
MLTX02-004CN-14080	FinalizeWaterProofing Worksfor Roofingand Wet Areas	6.00	100%	100%	03-Oct-26	08-Oct-26	28-Sep-26A	11-Oct-26A	$16,608.15	$1,660.815	$16,608.15	-600
MECHANICALWORK		9300	8893%	3647%	15-Sep-26	08-Nov-26	15-Aug-26A	29-Nov-26	$3,852,151.13	$158,018.25	$4,312,851.13	-4400
HVAC SYSTEM		1000	4755%	4755%	12-Oct-26	08-Nov-26	27-Sep-26A	29-Nov-26	$1,126,000	$1,312,500	$27,885.00	-3000
MLTX02-004CN-14160	Installand FinishHVAC and VentilationWorksIncludingSplitAir Units	6.00	0%	0%	02-Nov-26	08-Nov-26	22-Nov-26	29-Nov-26	$000	$000	$14,625.00	0.00
MLTX02-004CN-14150	Preliminary HVAC and Ventilation Works	3.00	100%	100%	12-Oct-26	14-Oct-26	27-Sep-26A	27-Sep-26A	$9,360.00	$9,360.00	$9,360.00	2.00
MLTX02-004CN-14170	Exhaust, Air Ducts Installationwithall Accessories	7.00	100%	100%	15-Oct-26	22-Oct-26	27-Sep-26A	27-Sep-26A	$3,900.00	$3,900.00	$3,900.00	6.00
WATERSUPPLY SYSTEM		6900	1889%	1889%	17-Sep-26	18-Oct-26	15-Aug-26A	07-Nov-26	$2,521,275.00	$476,775.00	$2,524,275.00	-4600
MLTX02-004CN-14200	Installing ofBooster PumpUnitsIncluding fttings and accessories	5.00	100%	0%	08-Oct-26	13-Oct-26	02-Nov-26	07-Nov-26	$91,000.00	$000	$91,000.00	0.00
MLTX02-004CN-14210	Installing ofGRP Tanks	5.00	100%	0%	03-Oct-26	07-Oct-26	27-Oct-26	01-Nov-26	$1,040,000.00	$000	$1,040,000.00	0.00
MLTX02-004CN-14600	Installing ofValvesand ftings	4.00	100%	0%	21-Sep-26	26-Sep-26	27-Oct-26	31-Oct-26	$9,750.00	$000	$9,750.00	0.00
MLTX02-004CN-14180	Installing ofPPR Pipes andFittings for WaterNetwork	3.00	100%	100%	17-Sep-26	20-Sep-26	15-Aug-26A	15Aug-26A	$6,922.50	$6,922.50	$6,922.50	2.00
MLTX02-004CN-14190	Installing ofHDPE Pipes andValvesforWaterSupplyNetwok	5.00	100%	100%	27-Sep-26	01-Oct-26	05-Oct-26A	10-Oct-26A	$3,900.00	$3,900.00	$39000.00	0.00

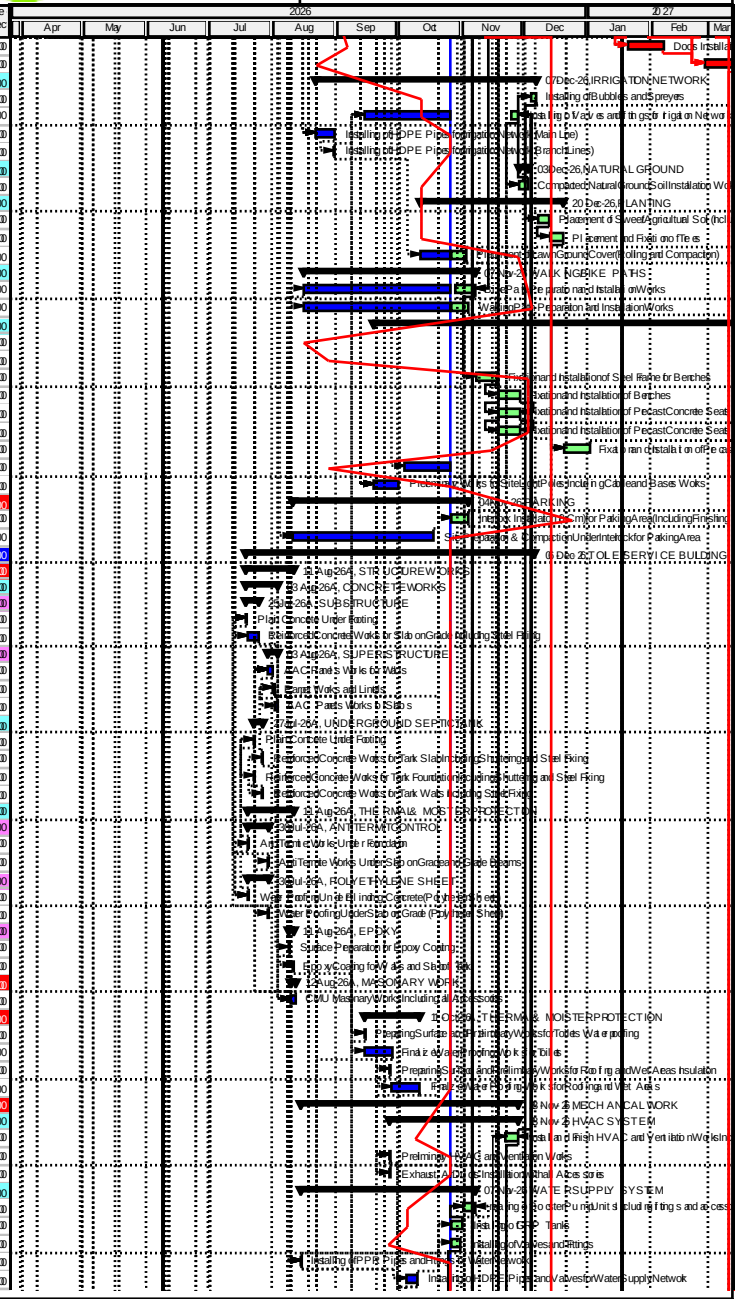

© Oracle Corporation

ActivityID	ActivityName	Orginal Duration	Schedule %	Performance% Complete	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Variance - BL Project
MLTX02-00-ACN-14690	Installing ofWater Heater	4.00	100%	100%	14-Oct-26	18Oct-26	08-Oct-26A	11Oct-26A	$1,755.00	$1755.00	$1,755.00	1.00
SEWERDRAIN AGESYSTEM		8100	7921%	6428%	15-Sep-26	29Oct-26	15-Aug-26A	18Nov-26	$1,196,277.63	$970,870.75	$1,510,262.63	-4400
MLTX02-00-ACN-14230	Installing ofPlumping Fixturesand Accessories	4.00	100%	0%	29-Sep-26	03Oct-26	01-Nov-26	04Nov-26	$10,359.38	$000	$10359.38	0.00
MLTX02-00-ACN-14680	Installing Inspection Chamber forSewageNetwork	5.00	100%	0%	17-Sep-26	22Sep-26	27-Oct-26	01Nov-26	$12,187.50	$000	$12187.50	0.00
MLTX02-00-ACN-14700	Installing ofToilet Fixturesand Accessories Such as Cbsetsand Basins	3.00	0%	0%	27-Oct-26	29Oct-26	16-Nov-26	18Nov-26	$000	$000	$31395.00	0.00
MLTX02-00-ACN-14220	Installing UPVC Pipes for Sewage Network	2.00	100%	100%	15-Sep-26	16Sep-26	15-Aug-26A	15Aug-26A	$1,176,825	$1,176,825	$11768.25	1.00
MLTX02-00-ACN-14610	Installing UPVC Pipes for ExternalConnecton for Sewage Network	4.00	100%	100%	24-Sep-26	28Sep-26	05-Oct-26A	11Oct-26A	$8,512,250	$8,512,250	$85312.50	-200
FIREPROTECTION		4.00	0%	0%	04-Nov-26	08Nov-26	24-Nov-26	28Nov-26	$000	$000	$1,950.00	0.00
MLTX02-00-ACN-14240	Installing ofFireFighting Extinguisherand accessories (PIE-1, PIE-2)	4.00	0%	0%	04-Nov-26	08Nov-26	24-Nov-26	28Nov-26	$000	$000	$1,950.00	0.00
ELECTRICAL WORKS		9600	3366%	5087%	15-Sep-26	16Nov-26	15-Aug-26A	06Dec-26	$7,283,250	$110,078,990	$2,164,013.38	-4300
ROUGH-IN WORKS		2400	100%	100%	15-Sep-26	26Sep-26	15-Aug-26A	29Aug-26A	$7,283,250	$7,283,250	$728232.50	-300
MLTX02-00-ACN-14280	Preleminary Woks forCableWorks	9.00	100%	100%	15-Sep-26	26Sep-26	15-Aug-26A	29Aug-26A	$1,070,004	$1,070,004	$10700.04	-300
MLTX02-00-ACN-14290	Preleminary Woks forSockets andPowerPoints	9.00	100%	100%	15-Sep-26	26Sep-26	15-Aug-26A	29Aug-26A	$92,309.91	$92,309.91	$9230.91	-300
MLTX02-00-ACN-14310	Preleminary Woks forLightingWorks	9.00	100%	100%	15-Sep-26	26Sep-26	15-Aug-26A	29Aug-26A	$97,500.00	$97,500.00	$9750.00	-300
MLTX02-00-ACN-14330	Preleminary Woks forData& TelecommunicationSystem	9.00	100%	100%	15-Sep-26	26Sep-26	15-Aug-26A	29Aug-26A	$1,228,500	$1,228,500	$12285.00	-300
MLTX02-00-ACN-14370	Preleminary Woks forSecurity and Access Contol System	9.00	100%	100%	15-Sep-26	26Sep-26	15-Aug-26A	29Aug-26A	$1,526,655	$1,526,655	$15266.55	-300
MLTX02-00-ACN-14660	Preleminary Woks forEarthing Works	9.00	100%	100%	15-Sep-26	26Sep-26	15-Aug-26A	29Aug-26A	$1,560,000	$1,560,000	$15600.00	-300
FIXTURE WORKS		2100	0%	2594%	02-Nov-26	16Nov-26	05-Oct-26A	06Dec-26	$000	$972,816.49	$1,485,618.88	-4100
MLTX02-00-ACN-14250	Installing ofFireautomationand Fie Alarm System	7.00	0%	0%	09-Nov-26	16Nov-26	29-Nov-26	06Dec-26	$000	$000	$34320.00	0.00
MLTX02-00-ACN-14320	Installing andFinalize Worksof Lighting Woks indudingLightFixtures	4.00	0%	0%	04-Nov-26	08Nov-26	24-Nov-26	28Nov-26	$000	$000	$16050.00	0.00
MLTX02-00-ACN-14340	Installing Data andTelecommunicaton System with allAccessories	4.00	0%	0%	04-Nov-26	08Nov-26	24-Nov-26	28Nov-26	$000	$000	$18427.50	0.00
MLTX02-00-ACN-14380	Installing andFinalize Worksof Securityand Access ControlSystem	6.00	0%	0%	02-Nov-26	08Nov-26	22-Nov-26	28Nov-26	$000	$000	$22899.83	0.00
MLTX02-00-ACN-14400	Installing andFinalize Worksof Lightning Protection System	6.00	0%	0%	02-Nov-26	08Nov-26	22-Nov-26	28Nov-26	$000	$000	$14625.00	0.00
MLTX02-00-ACN-14300	Installing andFinalize Worksof Sockets and PowerPoints	4.00	0%	100%	04-Nov-26	08Nov-26	05-Oct-26A	10Oct-26A	$000	$13,846.49	$13846.49	-100
MLTX02-00-ACN-14390	Installing andFinalize Worksof EarthingWorks	6.00	0%	100%	02-Nov-26	08Nov-26	05-Oct-26A	11Oct-26A	$000	$23,400.00	$23400.00	0.00
DOORS/WINDOWS		4200	40%	1429%	15-Sep-26	30Nov-26	07-Oct-26A	25Nov-26	$2,730,000	$9750.00	$68250.00	22.00
MLTX02-004CN-14470	FinalizeGlazzedCurtain Wall Works	4.00	0%	0%	02-Nov-26	05Nov-26	22-Nov-26	25Nov-26	$000	$000	$35100.00	0.00
MLTX02-004CN-14150	Preleminary Woks ForWindows/CutainWall	2.00	100%	0%	15-Sep-26	16Sep-26	27-Oct-26	28Oct-26	$23,400.00	$000	$23400.00	0.00
MLTX02-004CN-14090	Preleminary Woks ForDoors	3.00	100%	100%	15-Sep-26	17Sep-26	08-Oct-26A	10Oct-26A	$3,900.00	$3,900.00	$3900.00	1.00
MLTX02-004CN-14100	FinalizeMetalDoorsfor Toilets Building	1200	0%	100%	17-Nov-26	30Nov-26	07-Oct-26A	12Oct-26A	$000	$5,850.00	$5850.00	7.00
METALWORKS		900	85%	100%	12-Oct-26	29Oct-26	16-Sep-26A	27Sep-26A	$8,287.50	$9750.00	$9750.00	7.00
MLTX02-004CN-14040	Installationof GalvanizedSteelLadder	8.00	100%	100%	12-Oct-26	20Oct-26	27-Sep-26A	27Sep-26A	$5,850.00	$5850.00	$5850.00	7.00
MLTX02-004CN-14020	Installationof GalvanizedSteelRoofScupper	8.00	62.5%	100%	21-Oct-26	29Oct-26	16-Sep-26A	16Sep-26A	$2,437.50	$3900.00	$3900.00	7.00
FINISHING WORKS		5900	8834%	5336%	27-Sep-26	17Nov-26	29-Aug-26A	23Nov-26	$1,916,191.50	$7,225,791.99	$1,354,141.50	-2900
FLOORFINISHES		4100	9318%	8295%	30-Sep-26	17Nov-26	01-Oct-26A	31Oct-26	$1,599,000	$1,423,500	$17160.00	16.00
MLTX02-00-ACN-14480	Granite TilesFloorFinish Woks	4.00	100%	0%	05-Oct-26	08Oct-26	27-Oct-26	31Oct-26	$2,925.00	$000	$2925.00	0.00
MLTX02-00-ACN-14110	Ceramic Tiles Floor FinishWorks	4.00	100%	100%	30-Sep-26	04Oct-26	01-Oct-26A	04Oct-26A	$11,895.00	$11,895.00	$11895.00	2.00
MLTX02-00-ACN-14490	EpoxyCoaton Concete floor	1000	0%	100%	07-Nov-26	17Nov-26	07-Oct-26A	10Oct-26A	$000	$1170.00	$1,170.00	7.00
MLTX02-00-ACN-14500	Ceramic SkirtingTiles Finish Woks	2.00	100%	100%	10-Oct-26	11Oct-26	05-Oct-26A	07Oct-26A	$1,170.00	$1170.00	$1,170.00	-100
WALLFINISHES		5300	8608%	4863%	27-Sep-26	03Nov-26	29-Aug-26A	23Nov-26	$9,944,775	$5,109,652.50	$1,050,725.00	-4100
MLTX02-00-ACN-14460	Phendic Patitions for Toilets	5.00	100%	0%	21-Oct-26	26Oct-26	10-Nov-26	15Nov-26	$31,200.00	$000	$31200.00	0.00
MLTX02-00-ACN-14570	Glass Partitions includingallaccessoriesand doors	5.00	0%	0%	27-Oct-26	01Nov-26	16-Nov-26	21Nov-26	$000	$000	$12285.00	0.00
MLTX02-00-ACN-14580	Granite Cappingfor Parpet	2.00	100%	0%	10-Oct-26	11Oct-26	27-Oct-26	28Oct-26	$8,151.00	$000	$8,151.00	0.00
MLTX02-00-ACN-14670	PaintingFinishWorks forIntenalWalls	2.00	0%	0%	02-Nov-26	03Nov-26	22-Nov-26	23Nov-26	$000	$000	$2,340.00	0.00
MLTX02-00-ACN-14120	Preleminary Woks for Wall Finish Worksincluding Plastering (Intenal)	3.00	100%	100%	27-Sep-26	29Sep-26	29-Aug-26A	09Sep-26A	$18,369.00	$18,369.00	$18369.00	-800
MLTX02-00-ACN-14430	Preleminary Woks for Wall Finish Works(External)	8.00	100%	100%	27-Sep-26	05Oct-26	09-Sep-26A	10Sep-26A	$6,552.00	$6,552.00	$6552.00	6.00
MLTX02-00-ACN-14440	PaintingFinishWorks forExtenal Walls	3.00	100%	100%	06-Oct-26	08Oct-26	11-Oct-26A	13Oct-26A	$10,478.00	$10,478.00	$10478.00	0.00
MLTX02-00-ACN-14450	Ceramic Finish Worksfor Walls	6.00	100%	100%	05-Oct-26	11Oct-26	28-Sep-26A	29Sep-26A	$15,697.50	$15,697.50	$15697.50	5.00
CELLING FINISHES		2300	100%	5254%	30-Sep-26	24Oct-26	07-Oct-26A	10Nov-26	$13,182.00	$6926.40	$13182.00	-900
MLTX02-00-ACN-14710	PaintingFinishWorks forCeiling	3.00	100%	0%	21-Oct-26	24Oct-26	08-Nov-26	10Nov-26	$1,638.00	$000	$1,638.00	0.00
MLTX02-00-ACN-14730	Preleminary Woks for Ceiling Painting Works	1000	100%	0%	30-Sep-26	11Oct-26	27-Oct-26	07Nov-26	$4,617.60	$000	$4,617.60	0.00
MLTX02-00-ACN-14720	Gypsum BoardSuspended Ceiling finishWorksForCeiling	5.00	100%	100%	15-Oct-26	20Oct-26	07-Oct-26A	12Oct-26A	$6,926.40	$6926.40	$6926.40	0.00
SPECIALITES WORK		2600	25%	0%	04-Oct-26	15Nov-26	05-Nov-26	05Dec-26	$1,462,500	$000	$58506.48	11.00
MLTX02-004CN-14130	SantaryFixtures andAccessoriesWorks	4.00	100%	0%	04-Oct-26	07Oct-26	05-Nov-26	09Nov-26	$1,462,500	$000	$14625.00	0.00
MLTX02-004CN-14140	Installationof MODON Logo ontheentrance	1000	0%	0%	04-Nov-26	15Nov-26	24-Nov-26	05Dec-26	$000	$000	$19506.48	0.00
MLTX02-004CN-14190	Installationof PhenticLocker	2.00	0%	0%	27-Oct-26	28Oct-26	16-Nov-26	17Nov-26	$000	$000	$24375.00	0.00
TESTING & COMMISSIONING		9500	0%	0%	01-Dec-26	18Jan-27	08-Dec-26	01Apr-27	$000	$000	$0.00	-5300
MLTX02-004TC-11920	Testing and Commissioning forMEP Woks for PlaygroundArea	8.00	0%	0%	05-Jan-27	13Jan-27	17-Mar-27	25Mar-27	$000	$000	$0.00	0.00
MLTX02-004TC-11930	Testing and Commissioning forMEP Woks for ToiletServiceBuilding	1500	0%	0%	01-Dec-26	17Dec-26	08-Dec-26	24Dec-26	$000	$000	$0.00	0.00
MLTX02-004TC-11940	Testing and Commissioning forMEP Woks for LantscapeWorks	4.00	0%	0%	14-Jan-27	18Jan-27	29-Mar-27	01Apr-27	$000	$000	$0.00	0.00
ASIR		32500	3444%	3966%	26-Mar-26	24Jan-27	26-Mar-26A	18Apr-27	$3,643,213.82	$4194,757.30	$10578,073.08	-6800
MOBILIZATION		6300	0%	0%	26-Mar-26	10Jun-26	26-Mar-26A	10Jun-26A	$000	$000	$0.00	0.00
TOPOGRAPHICSURVEY		400	0%	0%	26-Mar-26	30Mar-26	26-Mar-26A	30Mar-26A	$000	$000	$0.00	0.00
MLTX02-004MB-1320	Site Survey Woks	4.00	100%	100%	26-Mar-26	30Mar-26	26-Mar-26A	30Mar-26A	$000	$000	$0.00	0.00
SITEFACILITES & OFFICES		4970	0%	0%	26-Mar-26	23May-26	26-Mar-26A	23May-26A	$000	$000	$0.00	0.00
MLTX02-004MB-1440	Manpower Mobalizaton	3170	100%	100%	16-Apr-26	23May-26	16-Apr-26A	23May-26A	$000	$000	$0.00	0.00
MLTX02-004MB-1430	Equipment Mobalization	2440	100%	100%	14-Apr-26	12May-26	14-Apr-26A	12May-26A	$000	$000	$0.00	0.00
MLTX02-004MB-1340	Site Layout Plan	4.00	100%	100%	26-Mar-26	30Mar-26	26-Mar-26A	30Mar-26A	$000	$000	$0.00	0.00
MLTX02-004MB-1350	Clear & Grub forOffices & AccessRoad	3.00	100%	100%	31-Mar-26	02Apr-26	31-Mar-26A	02Apr-26A	$000	$000	$0.00	0.00
MLTX02-004MB-1360	ConstuctSiteAccess Roads	4.00	100%	100%	31-Mar-26	04Apr-26	31-Mar-26A	04Apr-26A	$000	$000	$0.00	0.00
MLTX02-004MB-1370	ConstuctTemporay Fence	3175	100%	100%	15-Apr-26	21May-26	15-Apr-26A	21May-26A	$000	$000	$0.00	0.00

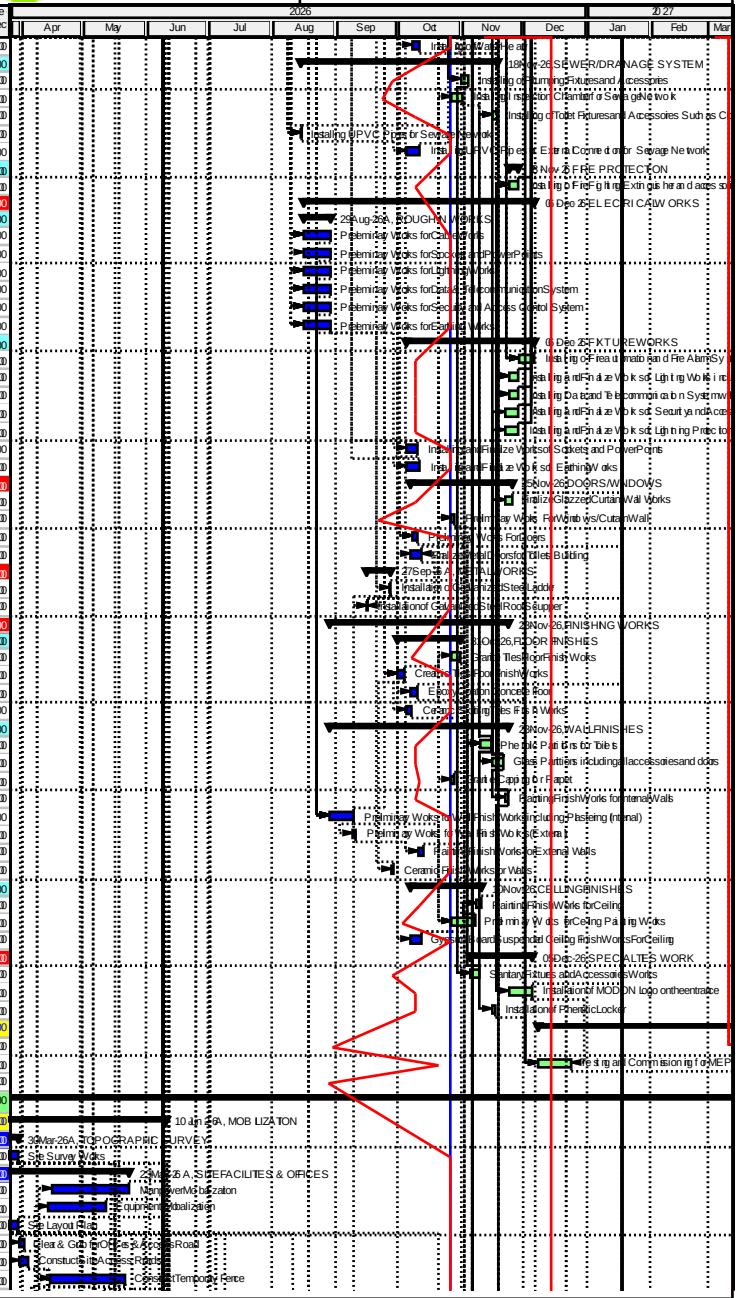


Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work

TASK filter: All Activities


© Oracle Corporation

ActivityID	ActivityName	Orginal Duration	Schedule %	Performance% Complete	BL Project Stat	BL Project Finish	Stat	Finish	Planned Value Cos	Earned Value Cos	Budgeted Tot Cos	Variance - BL Project
MLTX02-004MB-1380	ConstuctSiteOffices & Storage	1880	100%	100%	20 Apr 26	11May-26	20 Apr 26 A	11May-26A	$000	$000	$0.00	0.00
MLTX02-004MB-1390	InstallProject Signs	3.00	100%	100%	21 Apr 26	23Apr-26	21 Apr 26 A	23Apr-26A	$000	$000	$0.00	0.00
MLTX02-004MB-1400	InstallSiteFacilities	2355	100%	100%	12 Apr 26	09May-26	12 Apr 26 A	09May-26A	$000	$000	$0.00	0.00
MLTX02-004MB-1410	Electrical Works & Connections	2695	100%	100%	12 Apr 26	12May-26	12 Apr 26 A	12May-26A	$000	$000	$0.00	0.00
MLTX02-004MB-1420	ConstuctParking Sheds	2575	100%	100%	12 Apr 26	12May-26	12 Apr 26 A	12May-26A	$000	$000	$0.00	0.00
PRELIMINARY SUBMITTALS		5900	0%	0%	31 Mar 26	10Jun-26	31 Mar 26 A	10Jun-26A	$000	$000	$0.00	0.00
PREPARATIONS& SUBMITTALBY CONTRACTORS		2700	0%	0%	31 Mar 26	30Apr-26	31 Mar 26 A	30Apr-26A	$000	$000	$0.00	0.00
MLTX02-004MB-1540	Preparation andSubmittalofDetaledWorkOrderProgramme(Baseline)	2500	100%	100%	31 Mar 26	28Apr-26	31 Mar 26 A	28Apr-26A	$000	$000	$0.00	0.00
MLTX02-004MB-1550	Preparation andSubmittalofProject Execution Plan	2700	100%	100%	31 Mar 26	30Apr-26	31 Mar 26 A	30Apr-26A	$000	$000	$0.00	0.00
MLTX02-004MB-1560	Submissionof Contactor Project Quality Plan	1000	100%	100%	31 Mar 26	11Apr-26	31 Mar 26 A	11Apr-26A	$000	$000	$0.00	0.00
MLTX02-004MB-1570	Submissionof Construction Safety& EnvironmentalManagement Plan	1000	100%	100%	31 Mar 26	11Apr-26	31 Mar 26 A	11Apr-26A	$000	$000	$0.00	0.00
MLTX02-004MB-1580	Preparation andSubmittalofOrganization Chat	8.00	100%	100%	31 Mar 26	08Apr-26	31 Mar 26 A	08Apr-26A	$000	$000	$0.00	0.00
MLTX02-004MB-1590	Preparation andSubmittalofCommunication Plan	8.00	100%	100%	31 Mar 26	08Apr-26	31 Mar 26 A	08Apr-26A	$000	$000	$0.00	0.00
APPROVALS BYEMPLOYERS		5100	0%	0%	09 Apr 26	10Jun-26	09 Apr 26 A	10Jun-26A	$000	$000	$0.00	0.00
MLTX02-004MB-1680	Appoval of DetailedWorkOrderProgramme (Baseline)	1.00	100%	100%	29 Apr 26	29Apr-26	29 Apr 26 A	29Apr-26A	$000	$000	$0.00	0.00
MLTX02-004MB-1690	Appoval of Project Execution Plan	1.00	100%	100%	13 May-26	13May-26	13 May 26 A	13May-26A	$000	$000	$0.00	0.00
MLTX02-004MB-1700	Appoval of ContactorProject QualityPlan	1900	100%	100%	09 Apr 26	30Apr-26	09 Apr 26 A	30Apr-26A	$000	$000	$0.00	0.00
MLTX02-004MB-1710	Appoval of Constuction Safety & EnvironmentalManagement Plan	1.00	100%	100%	10 Jun 26	10Jun-26	10 Jun 26 A	10Jun-26A	$000	$000	$0.00	0.00
MLTX02-004MB-1720	Appoval of Organization Chat	1800	100%	100%	09 Apr 26	29Apr-26	09 Apr 26 A	29Apr-26A	$000	$000	$0.00	0.00
MLTX02-004MB-1730	Appoval of Communication Plan	1000	100%	100%	09 Apr 26	20Apr-26	09 Apr 26 A	20Apr-26A	$000	$000	$0.00	0.00
ENGINEERING		21200	0%	0%	31 Mar 26	02Sep-26	31 Mar 26 A	07Dec-26	$000	$000	$0.00	-8100
SHOP DRAWINGS		14100	0%	0%	31 Mar 26	18Jul-26	31 Mar 26 A	26Aug-26A	$000	$000	$0.00	-3400
SHOP DRAWINGS SUBMISSION		14100	0%	0%	31 Mar 26	18Jul-26	31 Mar 26 A	25Aug-26A	$000	$000	$0.00	-3300
SHOP DRAWINGSUBMITTALS FOR EARTHINGWORKS		5800	0%	0%	31 Mar 26	09Jun-26	31 Mar 26 A	09Jun-26A	$000	$000	$0.00	0.00
MLTX02-004EN-1790	ShopDWG SubmittalforLayoutPlan	1600	100%	100%	31 Mar 26	18Apr-26	31 Mar 26 A	18Apr-26A	$000	$000	$0.00	0.00
MLTX02-004EN-1800	ShopDWG SubmittalforSetting Out	4420	100%	100%	31 Mar 26	21May-26	31 Mar 26 A	21May-26A	$000	$000	$0.00	0.00
MLTX02-004EN-1810	ShopDWG SubmittalforGrading Layout Plan	2500	100%	100%	31 Mar 26	28Apr-26	31 Mar 26 A	28Apr-26A	$000	$000	$0.00	0.00
MLTX02-004EN-1820	ShopDWG SubmittalforCurb Setting OutPoints	1.00	100%	100%	21 May-26	21May-26	21 May 26 A	21May-26A	$000	$000	$0.00	0.00
MLTX02-004EN-1830	ShopDWG SubmittalforSigning & MakingLayoutPlan	1.00	100%	100%	09 Jun 26	09Jun-26	09 Jun 26 A	09Jun-26A	$000	$000	$0.00	0.00
MLTX02-004EN-1840	ShopDWG SubmittalforStandards Details	1.00	100%	100%	21 May-26	21May-26	21 May 26 A	21May-26A	$000	$000	$0.00	0.00
SHOP DRAWINGSUBMITTALS FOR SERVICE/TOILETWORKS		14100	0%	0%	31 Mar 26	18Jul-26	31 Mar 26 A	25Aug-26A	$000	$000	$0.00	-3300
ARCHITECTURE WORKS		1200	0%	0%	31 Mar 26	13Apr-26	31 Mar 26 A	13Apr-26A	$000	$000	$0.00	0.00
MLTX02-004EN-187	ShopDWG SubmittalforFloorPlan	1200	100%	100%	31 Mar 26	13Apr-26	31 Mar 26 A	13Apr-26A	$000	$000	$0.00	0.00
MLTX02-004EN-188	ShopDWG SubmittalforElevations	1200	100%	100%	31 Mar 26	13Apr-26	31 Mar 26 A	13Apr-26A	$000	$000	$0.00	0.00
MLTX02-004EN-189	ShopDWG SubmittalforSections	1200	100%	100%	31 Mar 26	13Apr-26	31 Mar 26 A	13Apr-26A	$000	$000	$0.00	0.00
MLTX02-004EN-190	ShopDWG SubmittalforCeiling Plan	1200	100%	100%	31 Mar 26	13Apr-26	31 Mar 26 A	13Apr-26A	$000	$000	$0.00	0.00
MLTX02-004EN-191	ShopDWG SubmittalforFinishes Plan	1200	100%	100%	31 Mar 26	13Apr-26	31 Mar 26 A	13Apr-26A	$000	$000	$0.00	0.00
MLTX02-004EN-192	ShopDWG SubmittalforToilet Details	1200	100%	100%	31 Mar 26	13Apr-26	31 Mar 26 A	13Apr-26A	$000	$000	$0.00	0.00
MLTX02-004EN-193	ShopDWG SubmittalforDoors\Windows Schedule	1200	100%	100%	31 Mar 26	13Apr-26	31 Mar 26 A	13Apr-26A	$000	$000	$0.00	0.00
STRUCTUREWORKS		2000	0%	0%	08 Apr 26	30Apr-26	08 Apr 26 A	30Apr-26A	$000	$000	$0.00	0.00
MLTX02-004EN-195	ShopDWG SubmittalforFoundationPlan	2000	100%	100%	08 Apr 26	30Apr-26	08 Apr 26 A	30Apr-26A	$000	$000	$0.00	0.00
MLTX02-004EN-196	ShopDWG SubmittalforGroundFloorFraming Plan	2000	100%	100%	08 Apr 26	30Apr-26	08 Apr 26 A	30Apr-26A	$000	$000	$0.00	0.00
MLTX02-004EN-197	ShopDWG SubmittalforSections/Details	2000	100%	100%	08 Apr 26	30Apr-26	08 Apr 26 A	30Apr-26A	$000	$000	$0.00	0.00
MECHANCALWORKS		3800	0%	0%	08 Apr 26	21May-26	08 Apr 26 A	21May-26A	$000	$000	$0.00	0.00
MLTX02-004EN-198	ShopDWG SubmittalforHVAC Plan	7.00	100%	100%	08 Apr 26	15Apr-26	08 Apr 26 A	15Apr-26A	$000	$000	$0.00	0.00
MLTX02-004EN-200	ShopDWG SubmittalforExhaustAirPlan	2000	100%	100%	08 Apr 26	30Apr-26	08 Apr 26 A	30Apr-26A	$000	$000	$0.00	0.00
MLTX02-004EN-201	ShopDWG SubmittalforHVAC Equipment Schedule	7.00	100%	100%	08 Apr 26	15Apr-26	08 Apr 26 A	15Apr-26A	$000	$000	$0.00	0.00
MLTX02-004EN-206	ShopDWG SubmittalforFireFighting Layout	6.00	100%	100%	08 Apr 26	14Apr-26	08 Apr 26 A	14Apr-26A	$000	$000	$0.00	0.00
MLTX02-004EN-207	ShopDWG SubmittalforWaterSupply Layout	1.00	100%	100%	06 May-26	06May-26	06 May 26 A	06May-26A	$000	$000	$0.00	0.00
MLTX02-004EN-208	ShopDWG SubmittalforWaterSupply Details	6.00	100%	100%	08 Apr 26	14Apr-26	08 Apr 26 A	14Apr-26A	$000	$000	$0.00	0.00
MLTX02-004EN-202	ShopDWG SubmittalforDrainage Layout	3800	100%	100%	08 Apr 26	21May-26	08 Apr 26 A	21May-26A	$000	$000	$0.00	0.00
MLTX02-004EN-203	ShopDWG SubmittalforDrainage Details	2000	100%	100%	08 Apr 26	30Apr-26	08 Apr 26 A	30Apr-26A	$000	$000	$0.00	0.00
MLTX02-004EN-204	ShopDWG SubmittalforDut RoutingLayout	1.00	100%	100%	21 May-26	21May-26	21 May 26 A	21May-26A	$000	$000	$0.00	0.00
MLTX02-004EN-205	ShopDWG SubmittalforDiffusersLayout	6.00	100%	100%	08 Apr 26	14Apr-26	08 Apr 26 A	14Apr-26A	$000	$000	$0.00	0.00
ELECTRCALWORKS		13400	0%	0%	08 Apr 26	18Jul-26	08 Apr 26 A	25Aug-26A	$000	$000	$0.00	-3300
MLTX02-004EN-210	ShopDWG SubmittalforLighting layout	1000	100%	100%	08 Apr 26	19Apr-26	08 Apr 26 A	19Apr-26A	$000	$000	$0.00	0.00
MLTX02-004EN-211	ShopDWG SubmittalforPower layout	1.00	100%	100%	06 May-26	06May-26	06 May 26 A	06May-26A	$000	$000	$0.00	0.00
MLTX02-004EN-212	ShopDWG SubmittalforPower SingleLineDiagram	1.00	100%	100%	06 May-26	06May-26	06 May 26 A	06May-26A	$000	$000	$0.00	0.00
MLTX02-004EN-213	ShopDWG SubmittalforPanelBoardSchedules	1.00	100%	100%	06 May-26	06May-26	06 May 26 A	06May-26A	$000	$000	$0.00	0.00
MLTX02-004EN-214	ShopDWG SubmittalforLighting Installation Details	1100	100%	100%	08 Apr 26	20Apr-26	08 Apr 26 A	20Apr-26A	$000	$000	$0.00	0.00
MLTX02-004EN-215	ShopDWG SubmittalforPower Installation Details	1.00	100%	100%	06 May-26	06May-26	06 May 26 A	06May-26A	$000	$000	$0.00	0.00
MLTX02-004EN-216	ShopDWG SubmittalforCableTrayInstallation Details	1.00	100%	100%	06 May-26	06May-26	06 May 26 A	06May-26A	$000	$000	$0.00	0.00
MLTX02-004EN-217	ShopDWG SubmittalforManhole& Ducbank Details	1.00	100%	100%	06 May-26	06May-26	06 May 26 A	06May-26A	$000	$000	$0.00	0.00
MLTX02-004EN-218	ShopDWG SubmittalforGrounding Details	1.00	100%	100%	06 May-26	06May-26	06 May 26 A	06May-26A	$000	$000	$0.00	0.00
MLTX02-004EN-221	ShopDWG SubmittalforLightningProtecton Details	1000	100%	100%	08 Apr 26	19Apr-26	08 Apr 26 A	19Apr-26A	$000	$000	$0.00	0.00
MLTX02-004EN-219	ShopDWG SubmittalforFireAlarmInstallation Details	1100	100%	100%	08 Apr 26	20Apr-26	08 Apr 26 A	20Apr-26A	$000	$000	$0.00	0.00
MLTX02-004EN-224	ShopDWG SubmittalforCCTV Details	6.00	100%	100%	05 Jul-26	11Jul-26	25 Aug 26 A	25Aug-26A	$000	$000	$0.00	5.00
MLTX02-004EN-227	ShopDWG SubmittalforGrounding Layout	1.00	100%	100%	07 May-26	07May-26	07 May 26 A	07May-26A	$000	$000	$0.00	0.00
MLTX02-004EN-222	ShopDWG SubmittalforLightningProtecton System Layout	1000	100%	100%	08 Apr 26	19Apr-26	08 Apr 26 A	19Apr-26A	$000	$000	$0.00	0.00
MLTX02-004EN-220	ShopDWG SubmittalforFireAlarmLayout	1100	100%	100%	08 Apr 26	20Apr-26	08 Apr 26 A	20Apr-26A	$000	$000	$0.00	0.00
MLTX02-004EN-223	ShopDWG SubmittalforFireAlarmRiserDiagram	1100	100%	100%	08 Apr 26	20Apr-26	08 Apr 26 A	20Apr-26A	$000	$000	$0.00	0.00

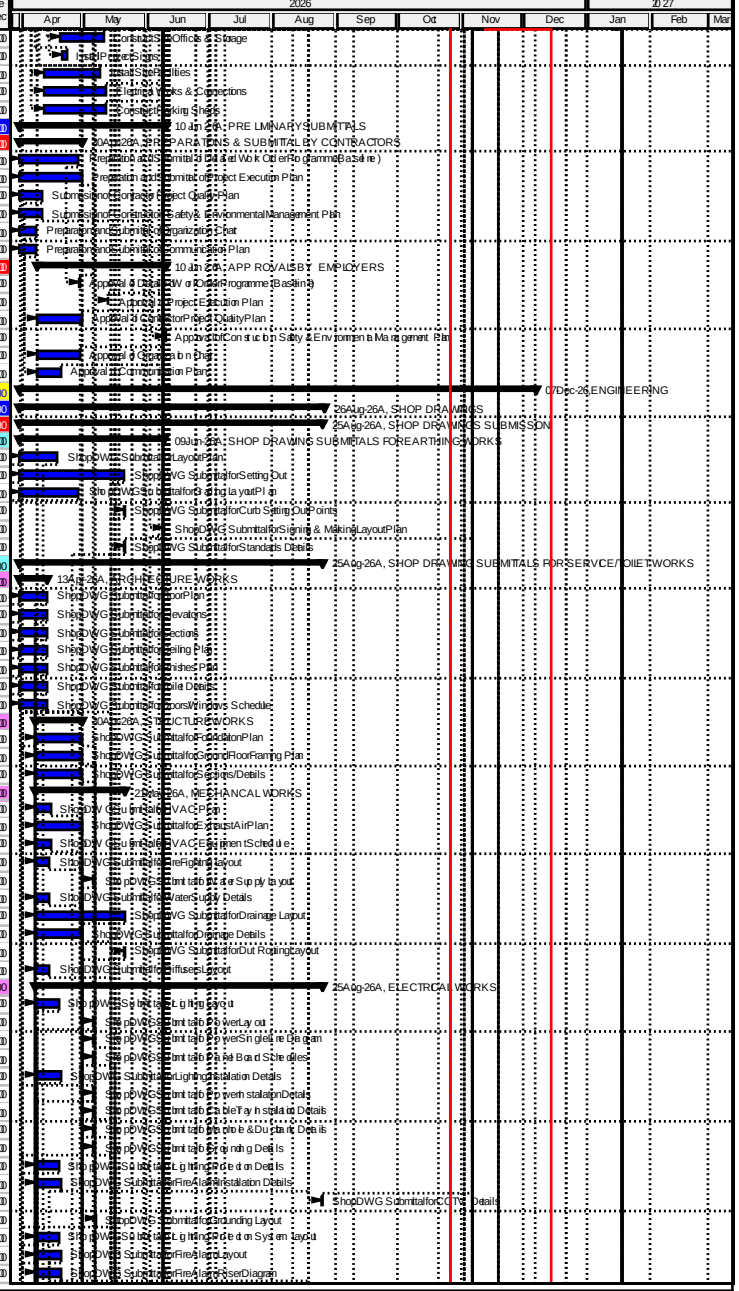


© Oracle Corporation

ActivityID	ActivityName	Orginal Duration	Schedule %	Performance% Complete	BL Project Stat	BL Project Finish	Stat	Finish	Planned Value Cos	Earned Value Cos	Budgeted Tot Cos	Variance - BL Project
MLTX02-004EN-22	ShopDWG SubmittalforCCTV Layout	6.00	100%	100%	05 Jul-25	11Jul-26	25 Aug 25 A	25Aug-26A	$000	$000	$0.00	5.00
MLTX02-004EN-22	ShopDWG SubmittalforCCTV Riser Diagram	6.00	100%	100%	12 Jul-25	18Jul-26	25 Aug 25 A	25Aug-26A	$000	$000	$0.00	5.00
MLTX02-004EN-22	ShopDWG SubmittalforTelephone & Data Layout	11.00	100%	100%	08 Apr 26	20Apr-26	08 Apr 26 A	20Apr-26A	$000	$000	$0.00	0.00
MLTX02-004EN-22	ShopDWG SubmittalforTelephone & Data Riser Diagram	11.00	100%	100%	08 Apr 26	20Apr-26	08 Apr 26 A	20Apr-26A	$000	$000	$0.00	0.00
SHOP DRAWINGS SUBMITTALS FOR PLAYGROUND WORKS		141.00	0%	0%	31 Mar 26	18Jul-26	31 Mar 26 A	25Aug-26A	$000	$000	$0.00	-33.00
ARCHITECTURE WORKS		39.00	0%	0%	31 Mar 26	14May-26	31 Mar 26 A	14May-26A	$000	$000	$0.00	0.00
MLTX02-004EN-23	ShopDWG SubmittalforPlayground Plan/Layout	16.00	100%	100%	31 Mar 26	18Apr-26	31 Mar 26 A	18Apr-26A	$000	$000	$0.00	0.00
MLTX02-004EN-23	ShopDWG SubmittalforFurniture& Marking	2.00	100%	100%	13 May-26	14May-26	13 May 25 A	14May-26A	$000	$000	$0.00	0.00
MLTX02-004EN-23	ShopDWG SubmittalforSections	16.00	100%	100%	31 Mar 26	18Apr-26	31 Mar 26 A	18Apr-26A	$000	$000	$0.00	0.00
MLTX02-004EN-23	ShopDWG SubmittalforInterlockPatten Plan	2.00	100%	100%	13 May-26	14May-26	13 May 25 A	14May-26A	$000	$000	$0.00	0.00
MLTX02-004EN-23	ShopDWG SubmittalforDoors\Windows Schedule	2.00	100%	100%	13 May-26	14May-26	13 May 25 A	14May-26A	$000	$000	$0.00	0.00
MLTX02-004EN-23	ShopDWG SubmittalforDome Internal Layout	2.00	100%	100%	13 May-26	14May-26	13 May 25 A	14May-26A	$000	$000	$0.00	0.00
STRUCTUREWORKS		2.00	0%	0%	13 May-26	14May-26	13 May 25 A	14May-26A	$000	$000	$0.00	0.00
MLTX02-004EN-23	ShopDWG SubmittalforAir Dome System	2.00	100%	100%	13 May-26	14May-26	13 May 25 A	14May-26A	$000	$000	$0.00	0.00
MLTX02-004EN-24	ShopDWG SubmittalforFoundationof AirDome	2.00	100%	100%	13 May-26	14May-26	13 May 25 A	14May-26A	$000	$000	$0.00	0.00
MLTX02-004EN-24	ShopDWG SubmittalforAnchorBoltLayoutof Air Dome	2.00	100%	100%	13 May-26	14May-26	13 May 25 A	14May-26A	$000	$000	$0.00	0.00
AIRDOMESYSTEM		2.00	0%	0%	13 May-26	14May-26	13 May 25 A	14May-26A	$000	$000	$0.00	0.00
MLTX02-004EN-24	ShopDWG SubmittalforAir Dome Structural Layout	2.00	100%	100%	13 May-26	14May-26	13 May 25 A	14May-26A	$000	$000	$0.00	0.00
MLTX02-004EN-24	ShopDWG SubmittalforMembrane PanelLayout	2.00	100%	100%	13 May-26	14May-26	13 May 25 A	14May-26A	$000	$000	$0.00	0.00
MLTX02-004EN-24	ShopDWG SubmittalforCableTension Layout	2.00	100%	100%	13 May-26	14May-26	13 May 25 A	14May-26A	$000	$000	$0.00	0.00
MLTX02-004EN-24	ShopDWG SubmittalforAirlock DoorDetails	2.00	100%	100%	13 May-26	14May-26	13 May 25 A	14May-26A	$000	$000	$0.00	0.00
MLTX02-004EN-24	ShopDWG SubmittalforEmergency ExitDetails	2.00	100%	100%	13 May-26	14May-26	13 May 25 A	14May-26A	$000	$000	$0.00	0.00
SPORTS EQUPMENT		2.00	0%	0%	13 May-26	14May-26	13 May 25 A	14May-26A	$000	$000	$0.00	0.00
MLTX02-004EN-25	ShopDWG SubmittalforFootball Turf Installation	2.00	100%	100%	13 May-26	14May-26	13 May 25 A	14May-26A	$000	$000	$0.00	0.00
MLTX02-004EN-25	ShopDWG SubmittalforBasketballCourtMarking	2.00	100%	100%	13 May-26	14May-26	13 May 25 A	14May-26A	$000	$000	$0.00	0.00
MLTX02-004EN-25	ShopDWG SubmittalforPadelCourtStructure	2.00	100%	100%	13 May-26	14May-26	13 May 25 A	14May-26A	$000	$000	$0.00	0.00
MECHANCALWORKS		20.00	0%	0%	08 Apr 26	30Apr-26	08 Apr 26 A	30Apr-26A	$000	$000	$0.00	0.00
MLTX02-004EN-25	ShopDWG SubmittalforHVAC Plan	20.00	100%	100%	08 Apr 26	30Apr-26	08 Apr 26 A	30Apr-26A	$000	$000	$0.00	0.00
MLTX02-004EN-25	ShopDWG SubmittalforExhaustAirPlan	20.00	100%	100%	08 Apr 26	30Apr-26	08 Apr 26 A	30Apr-26A	$000	$000	$0.00	0.00
ELECTRCALWORKS		96.00	0%	0%	23 May-26	18Jul-26	23 May 25 A	25Aug-26A	$000	$000	$0.00	-33.00
MLTX02-004EN-25	ShopDWG SubmittalforLighting layout	1.00	100%	100%	25 May-26	25May-26	25 May 25 A	25May-26A	$000	$000	$0.00	0.00
MLTX02-004EN-25	ShopDWG SubmittalforPower layout	1.00	100%	100%	01 Jul-25	01Jul-26	01 Jul-26A	01Jul-26A	$000	$000	$0.00	0.00
MLTX02-004EN-26	ShopDWG SubmittalforPower SingleLineDiagram	1.00	100%	100%	01 Jul-25	01Jul-26	01 Jul-26A	01Jul-26A	$000	$000	$0.00	0.00
MLTX02-004EN-26	ShopDWG SubmittalforPanelBoardSchedules	1.00	100%	100%	01 Jul-25	01Jul-26	01 Jul-26A	01Jul-26A	$000	$000	$0.00	0.00
MLTX02-004EN-25	ShopDWG SubmittalforPower Instalation Details	1.00	100%	100%	01 Jul-25	01Jul-26	01 Jul-26A	01Jul-26A	$000	$000	$0.00	0.00
MLTX02-004EN-26	ShopDWG SubmittalforFireAlarmInstallation Details	1.00	100%	100%	23 May-26	23May-26	23 May 25 A	23May-26A	$000	$000	$0.00	0.00
MLTX02-004EN-26	ShopDWG SubmittalforCCTV Details	6.00	100%	100%	05 Jul-25	11Jul-26	25 Aug 25 A	25Aug-26A	$000	$000	$0.00	5.00
MLTX02-004EN-26	ShopDWG SubmittalforFireAlarmLayout	1.00	100%	100%	23 May-26	23May-26	23 May 25 A	23May-26A	$000	$000	$0.00	0.00
MLTX02-004EN-26	ShopDWG SubmittalforFireAlarmRiserDiagram	1.00	100%	100%	23 May-26	23May-26	23 May 25 A	23May-26A	$000	$000	$0.00	0.00
MLTX02-004EN-26	ShopDWG SubmittalforCCTV Layout	6.00	100%	100%	05 Jul-25	11Jul-26	25 Aug 25 A	25Aug-26A	$000	$000	$0.00	5.00
MLTX02-004EN-26	ShopDWG SubmittalforCCTV Riser Diagram	6.00	100%	100%	12 Jul-25	18Jul-26	25 Aug 25 A	25Aug-26A	$000	$000	$0.00	5.00
SHOP DRAWINGS SUBMITTALS FOR LANDSCAPE WORKS		65.00	0%	0%	31 Mar 26	17Jun-26	31 Mar 26 A	17Jun-26A	$000	$000	$0.00	0.00
ARCHITECTURE WORKS		39.00	0%	0%	31 Mar 26	14May-26	31 Mar 26 A	14May-26A	$000	$000	$0.00	0.00
MLTX02-004EN-27	ShopDWG SubmittalforLandscape Layout	6.00	100%	100%	31 Mar 26	06Apr-26	31 Mar 26 A	06Apr-26A	$000	$000	$0.00	0.00
MLTX02-004EN-27	ShopDWG SubmittalforHardscape Plan	2.00	100%	100%	13 May-26	14May-26	13 May 25 A	14May-26A	$000	$000	$0.00	0.00
MLTX02-004EN-27	ShopDWG SubmittalforPlanting Plan	2.00	100%	100%	13 May-26	14May-26	13 May 25 A	14May-26A	$000	$000	$0.00	0.00
MLTX02-004EN-27	ShopDWG SubmittalforLandscape Details	2.00	100%	100%	13 May-26	14May-26	13 May 25 A	14May-26A	$000	$000	$0.00	0.00
MECHANCALWORKS		10.00	0%	0%	17 Jun 26	17Jun-26	17 Jun 26 A	17Jun-26A	$000	$000	$0.00	0.00
MLTX02-004EN-27	ShopDWG SubmittalforIrrigation Details	1.00	100%	100%	17 Jun 26	17Jun-26	17 Jun 26 A	17Jun-26A	$000	$000	$0.00	0.00
MLTX02-004EN-28	ShopDWG SubmittalforIrrigation Layout	1.00	100%	100%	17 Jun 26	17Jun-26	17 Jun 26 A	17Jun-26A	$000	$000	$0.00	0.00
ELECTRCALWORKS		10.00	0%	0%	23 May-26	23May-26	23 May 25 A	23May-26A	$000	$000	$0.00	0.00
MLTX02-004EN-28	ShopDWG SubmittalforLighting GeneralArrangement	1.00	100%	100%	23 May-26	23May-26	23 May 25 A	23May-26A	$000	$000	$0.00	0.00
MLTX02-004EN-28	ShopDWG SubmittalforLighting NetworkLayout	1.00	100%	100%	23 May-26	23May-26	23 May 25 A	23May-26A	$000	$000	$0.00	0.00
MLTX02-004EN-28	ShopDWG SubmittalforLighting Details	1.00	100%	100%	23 May-26	23May-26	23 May 25 A	23May-26A	$000	$000	$0.00	0.00
MLTX02-004EN-28	ShopDWG SubmittalforLighting SingleLine Diagram	1.00	100%	100%	23 May-26	23May-26	23 May 25 A	23May-26A	$000	$000	$0.00	0.00
SHOP DRAWINGS APPROVALS		129.00	0%	0%	07 Apr 26	11Jul-26	07 Apr 26 A	26Aug-26A	$000	$000	$0.00	-40.00
SHOP DRAWINGS APPROVALFOR EARTHINGWORKS		52.00	0%	0%	07 Apr 26	09Jun-26	07 Apr 26 A	09Jun-26A	$000	$000	$0.00	0.00
MLTX02-004EN-29	ShopDWG Appovalfor layoutPlan	6.00	100%	100%	18 Apr 26	23Apr-26	18 Apr 26 A	24Apr-26A	$000	$000	$0.00	0.00
MLTX02-004EN-29	ShopDWG Appovalfor SettingOut	0.00	100%	100%	21 May-26	21May-26	21 May 25 A	21May-26A	$000	$000	$0.00	0.00
MLTX02-004EN-29	ShopDWG Appovalfor GadingLayoutPlan	20.00	100%	100%	07 Apr 26	29Apr-26	07 Apr 26 A	29Apr-26A	$000	$000	$0.00	0.00
MLTX02-004EN-29	ShopDWG Appovalfor Cub SetingOut Points	1.00	100%	100%	21 May-26	21May-26	21 May 25 A	21May-26A	$000	$000	$0.00	0.00
MLTX02-004EN-29	ShopDWG Appovalfor Signing& Marking Layout Plan	1.00	100%	100%	09 Jun 26	09Jun-26	09 Jun 26 A	09Jun-26A	$000	$000	$0.00	0.00
MLTX02-004EN-29	ShopDWG Appovalfor Standards Details	1.00	100%	100%	21 May-26	21May-26	21 May 25 A	21May-26A	$000	$000	$0.00	0.00
SHOP DRAWINGS APPROVALFOR SERVICETOILETWORKS		111.00	0%	0%	14 Apr 26	11Jul-26	14 Apr 26 A	12Aug-26A	$000	$000	$0.00	-29.00
ARCHITECTURE WORKS		90.00	0%	0%	14 Apr 26	23Apr-26	14 Apr 26 A	24Apr-26A	$000	$000	$0.00	0.00
MLTX02-004EN-29	ShopDWG Appovalfor RoofPlan	9.00	100%	100%	14 Apr 26	23Apr-26	14 Apr 26 A	24Apr-26A	$000	$000	$0.00	0.00
MLTX02-004EN-29	ShopDWG Appovalfor Elevations	9.00	100%	100%	14 Apr 26	23Apr-26	14 Apr 26 A	24Apr-26A	$000	$000	$0.00	0.00
MLTX02-004EN-30	ShopDWG Appovalfor Sections	9.00	100%	100%	14 Apr 26	23Apr-26	14 Apr 26 A	24Apr-26A	$000	$000	$0.00	0.00
MLTX02-004EN-30	ShopDWG Appovalfor CeilingPlan	9.00	100%	100%	14 Apr 26	23Apr-26	14 Apr 26 A	24Apr-26A	$000	$000	$0.00	0.00
MLTX02-004EN-30	ShopDWG Appovalfor finishes Plan	9.00	100%	100%	14 Apr 26	23Apr-26	14 Apr 26 A	24Apr-26A	$000	$000	$0.00	0.00
MLTX02-004EN-30	ShopDWG Appovalfor ToiletDetals	9.00	100%	100%	14 Apr 26	23Apr-26	14 Apr 26 A	24Apr-26A	$000	$000	$0.00	0.00

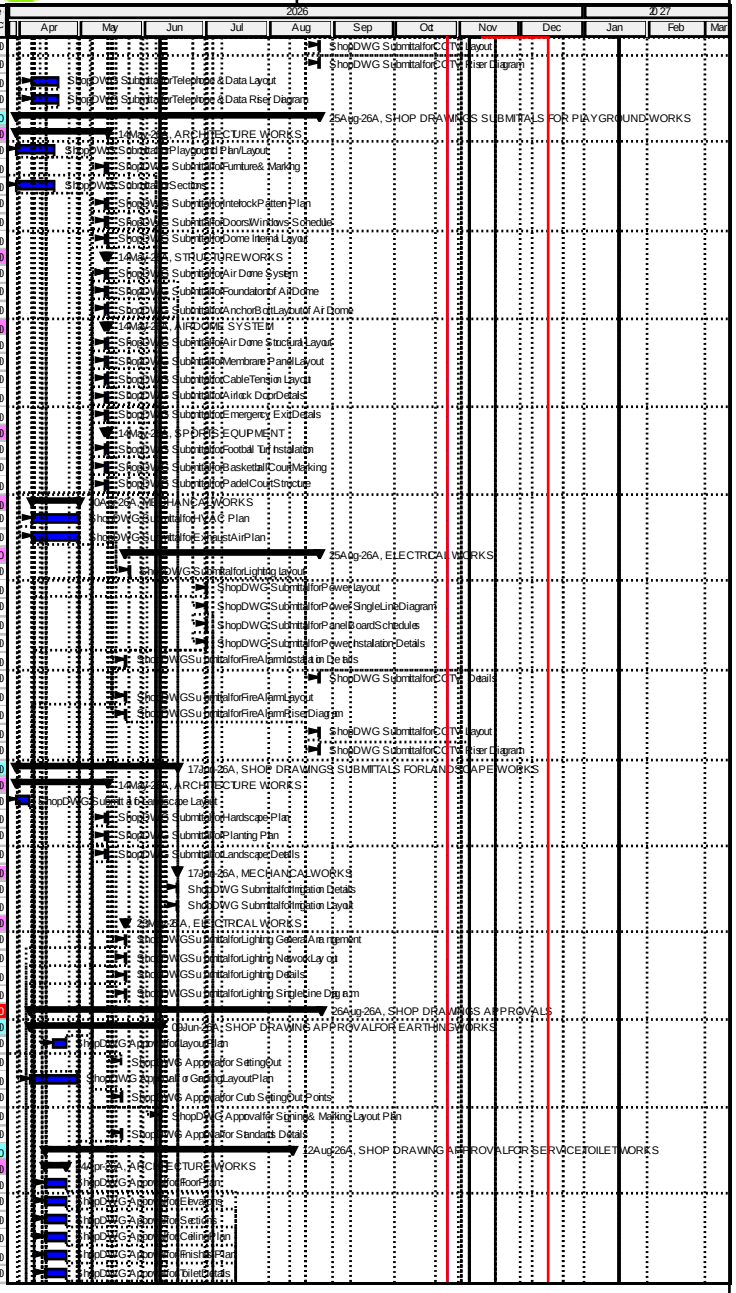


© Oracle Corporation

ActivityID	ActivityName	Orginal Duration	Schedule %	Performance% Complete	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Variance - BL Project
MLTX02-004EN-304	ShopDWG Appovalfor Doors/WindowsSchedule	9.00	100%	100%	14 Apr 26	23Apr-26	14 Apr 26 A	24Apr-26A	$000	$000	$0.00	0.00
STRUCTUREWORKS		2.00	0%	0%	13 May-26	14May-26	13 May 26 A	14May-26A	$000	$000	$0.00	0.00
MLTX02-004EN-306	ShopDWG Appovalfor Foundation Plan	2.00	100%	100%	13 May-26	14May-26	13 May 26 A	14May-26A	$000	$000	$0.00	0.00
MLTX02-004EN-307	ShopDWG Appovalfor Ground floorFraming Plan	2.00	100%	100%	13 May-26	14May-26	13 May 26 A	14May-26A	$000	$000	$0.00	0.00
MLTX02-004EN-308	ShopDWG Appovalfor SectionsDetails	2.00	100%	100%	13 May-26	14May-26	13 May 26 A	14May-26A	$000	$000	$0.00	0.00
MECHANCALWORKS		1300	0%	0%	07 May-26	21May-26	07 May 26 A	21May-26A	$000	$000	$0.00	0.00
MLTX02-004EN-310	ShopDWG Appovalfor HVACPlan	1.00	100%	100%	07 May-26	07May-26	07 May 26 A	07May-26A	$000	$000	$0.00	0.00
MLTX02-004EN-311	ShopDWG Appovalfor ExhaustAir Plan	1.00	100%	100%	07 May-26	07May-26	07 May 26 A	07May-26A	$000	$000	$0.00	0.00
MLTX02-004EN-312	ShopDWG Appovalfor HVACEquipment Schedule	4.00	100%	100%	07 May-26	11May-26	07 May 26 A	11May-26A	$000	$000	$0.00	0.00
MLTX02-004EN-317	ShopDWG Appovalfor Fire Fighting Layout	1.00	100%	100%	07 May-26	07May-26	07 May 26 A	07May-26A	$000	$000	$0.00	0.00
MLTX02-004EN-318	ShopDWG Appovalfor WaterSupplyLayout	1.00	100%	100%	07 May-26	07May-26	07 May 26 A	07May-26A	$000	$000	$0.00	0.00
MLTX02-004EN-319	ShopDWG Appovalfor WaterSupplyDetails	1.00	100%	100%	07 May-26	07May-26	07 May 26 A	07May-26A	$000	$000	$0.00	0.00
MLTX02-004EN-313	ShopDWG Appovalfor DrainageLayout	1.00	100%	100%	07 May-26	07May-26	07 May 26 A	07May-26A	$000	$000	$0.00	0.00
MLTX02-004EN-314	ShopDWG Appovalfor DrainageDetails	1.00	100%	100%	21 May-26	21May-26	21 May 26 A	21May-26A	$000	$000	$0.00	0.00
MLTX02-004EN-315	ShopDWG Appovalfor Duct RoutingLayout	1.00	100%	100%	07 May-26	07May-26	07 May 26 A	07May-26A	$000	$000	$0.00	0.00
MLTX02-004EN-316	ShopDWG Appovalfor Diffusers Layout	1.00	100%	100%	21 May-26	21May-26	21 May 26 A	21May-26A	$000	$000	$0.00	0.00
ELECTRCALWORKS		11000	0%	0%	15 Apr 26	11Jul-26	15 Apr 26 A	12Aug-26A	$000	$000	$0.00	-2800
MLTX02-004EN-321	ShopDWG Appovalfor Lighting Layout	1000	100%	100%	15 Apr 26	26Apr-26	15 Apr 26 A	26Apr-26A	$000	$000	$0.00	0.00
MLTX02-004EN-322	ShopDWG Appovalfor Power Layout	1000	100%	100%	15 Apr 26	26Apr-26	15 Apr 26 A	26Apr-26A	$000	$000	$0.00	0.00
MLTX02-004EN-323	ShopDWG Appovalfor Power Single line Diagram	1.00	100%	100%	23 May-26	23May-26	23 May 26 A	23May-26A	$000	$000	$0.00	0.00
MLTX02-004EN-324	ShopDWG Appovalfor Panel Board Schedules	1.00	100%	100%	23 May-26	23May-26	23 May 26 A	23May-26A	$000	$000	$0.00	0.00
MLTX02-004EN-325	ShopDWG Appovalfor Lighting InstallationDetails	1000	100%	100%	15 Apr 26	26Apr-26	15 Apr 26 A	26Apr-26A	$000	$000	$0.00	0.00
MLTX02-004EN-326	ShopDWG Appovalfor Power InstallationDetails	1000	100%	100%	15 Apr 26	26Apr-26	15 Apr 26 A	26Apr-26A	$000	$000	$0.00	0.00
MLTX02-004EN-327	ShopDWG Appovalfor Cable Tray InstallationDetails	1.00	100%	100%	23 May-26	23May-26	23 May 26 A	23May-26A	$000	$000	$0.00	0.00
MLTX02-004EN-328	ShopDWG Appovalfor Manhole& DuctbankDetails	1.00	100%	100%	23 May-26	23May-26	23 May 26 A	23May-26A	$000	$000	$0.00	0.00
MLTX02-004EN-329	ShopDWG Appovalfor Grounding Details	1.00	100%	100%	23 May-26	23May-26	23 May 26 A	23May-26A	$000	$000	$0.00	0.00
MLTX02-004EN-332	ShopDWG Appovalfor lightning Potection Details	1000	100%	100%	15 Apr 26	26Apr-26	15 Apr 26 A	26Apr-26A	$000	$000	$0.00	0.00
MLTX02-004EN-330	ShopDWG Appovalfor Fire Alarm Installation Details	6.00	100%	100%	21 Apr 26	27Apr-26	21 Apr 26 A	27Apr-26A	$000	$000	$0.00	0.00
MLTX02-004EN-335	ShopDWG Appovalfor CCTV Details	6.00	100%	100%	05 Jul-26	11Jul-26	12 Aug 26 A	12Aug-26A	$000	$000	$0.00	5.00
MLTX02-004EN-338	ShopDWG Appovalfor Grounding Layout	1.00	100%	100%	23 May-26	23May-26	23 May 26 A	23May-26A	$000	$000	$0.00	0.00
MLTX02-004EN-333	ShopDWG Appovalfor lightning Potection System Layout	1000	100%	100%	15 Apr 26	26Apr-26	15 Apr 26 A	26Apr-26A	$000	$000	$0.00	0.00
MLTX02-004EN-331	ShopDWG Appovalfor Fire Alarm layout	6.00	100%	100%	21 Apr 26	27Apr-26	21 Apr 26 A	27Apr-26A	$000	$000	$0.00	0.00
MLTX02-004EN-334	ShopDWG Appovalfor Fire Alarm Riser Diagram	6.00	100%	100%	21 Apr 26	27Apr-26	21 Apr 26 A	27Apr-26A	$000	$000	$0.00	0.00
MLTX02-004EN-336	ShopDWG Appovalfor CCTV Layout	6.00	100%	100%	05 Jul-26	11Jul-26	12 Aug 26 A	12Aug-26A	$000	$000	$0.00	5.00
MLTX02-004EN-339	ShopDWG Appovalfor CCTV RiserDiagam	6.00	100%	100%	05 Jul-26	11Jul-26	12 Aug 26 A	12Aug-26A	$000	$000	$0.00	5.00
MLTX02-004EN-337	ShopDWG Appovalfor Telephone & Data Layout	6.00	100%	100%	21 Apr 26	27Apr-26	21 Apr 26 A	27Apr-26A	$000	$000	$0.00	0.00
MLTX02-004EN-340	ShopDWG Appovalfor Telephone & Data Riser Diagram	6.00	100%	100%	21 Apr 26	27Apr-26	21 Apr 26 A	27Apr-26A	$000	$000	$0.00	0.00
SHOP DRAWIN GSAPPROVALFOR PLAYGROUND WORKS		12200	0%	0%	15 Apr 26	11Jul-26	15 Apr 26 A	26Aug-26A	$000	$000	$0.00	-4000
ARCHITECTURE WORKS		4500	0%	0%	19 Apr 26	13Jun-26	19 Apr 26 A	13Jun-26A	$000	$000	$0.00	0.00
MLTX02-004EN-343	ShopDWG Appovalfor Playground Plan/Layout	5.00	100%	100%	19 Apr 26	23Apr-26	19 Apr 26 A	24Apr-26A	$000	$000	$0.00	0.00
MLTX02-004EN-344	ShopDWG Appovalfor Furniture & Marking	1.00	100%	100%	13 Jun 26	13Jun-26	13 Jun 26 A	13Jun-26A	$000	$000	$0.00	0.00
MLTX02-004EN-345	ShopDWG Appovalfor Sections	5.00	100%	100%	19 Apr 26	23Apr-26	19 Apr 26 A	24Apr-26A	$000	$000	$0.00	0.00
MLTX02-004EN-346	ShopDWG Appovalfor Interlock PatternPlan	1.00	100%	100%	13 Jun 26	13Jun-26	13 Jun 26 A	13Jun-26A	$000	$000	$0.00	0.00
MLTX02-004EN-347	ShopDWG Appovalfor Doors/WindowsSchedule	1.00	100%	100%	13 Jun 26	13Jun-26	13 Jun 26 A	13Jun-26A	$000	$000	$0.00	0.00
MLTX02-004EN-348	ShopDWG Appovalfor Dome InternalLayout	1.00	100%	100%	13 Jun 26	13Jun-26	13 Jun 26 A	13Jun-26A	$000	$000	$0.00	0.00
STRUCTUREWORKS		1.00	0%	0%	24 Jun 26	24Jun-26	24 Jun 26 A	24Jun-26A	$000	$000	$0.00	0.00
MLTX02-004EN-350	ShopDWG Appovalfor Air DomeSystem	1.00	100%	100%	24 Jun 26	24Jun-26	24 Jun 26 A	24Jun-26A	$000	$000	$0.00	0.00
MLTX02-004EN-351	ShopDWG Appovalfor Foundation ofAirDome	1.00	100%	100%	24 Jun 26	24Jun-26	24 Jun 26 A	24Jun-26A	$000	$000	$0.00	0.00
MLTX02-004EN-352	ShopDWG Appovalfor Foundation ofAirDome	1.00	100%	100%	24 Jun 26	24Jun-26	24 Jun 26 A	24Jun-26A	$000	$000	$0.00	0.00
MLTX02-004EN-353	ShopDWG Appovalfor Anchor Bolt layoutof AirDome	1.00	100%	100%	24 Jun 26	24Jun-26	24 Jun 26 A	24Jun-26A	$000	$000	$0.00	0.00
AIRDOMESYS TEM		1.00	0%	0%	13 Jun 26	13Jun-26	13 Jun 26 A	13Jun-26A	$000	$000	$0.00	0.00
MLTX02-004EN-355	ShopDWG Appovalfor Air DomeStructuralLayout	1.00	100%	100%	13 Jun 26	13Jun-26	13 Jun 26 A	13Jun-26A	$000	$000	$0.00	0.00
MLTX02-004EN-356	ShopDWG Appovalfor MembranePanelLayout	1.00	100%	100%	13 Jun 26	13Jun-26	13 Jun 26 A	13Jun-26A	$000	$000	$0.00	0.00
MLTX02-004EN-357	ShopDWG Appovalfor Cable TensionLayout	1.00	100%	100%	13 Jun 26	13Jun-26	13 Jun 26 A	13Jun-26A	$000	$000	$0.00	0.00
MLTX02-004EN-358	ShopDWG Appovalfor AirlockDoorDetails	1.00	100%	100%	13 Jun 26	13Jun-26	13 Jun 26 A	13Jun-26A	$000	$000	$0.00	0.00
MLTX02-004EN-359	ShopDWG Appovalfor EmergencyExitDetails	1.00	100%	100%	13 Jun 26	13Jun-26	13 Jun 26 A	13Jun-26A	$000	$000	$0.00	0.00
SPORTS EQUPMENT		1.00	0%	0%	13 Jun 26	13Jun-26	13 Jun 26 A	13Jun-26A	$000	$000	$0.00	0.00
MLTX02-004EN-361	ShopDWG Appovalfor Footbal Tuf Installation	1.00	100%	100%	13 Jun 26	13Jun-26	13 Jun 26 A	13Jun-26A	$000	$000	$0.00	0.00
MLTX02-004EN-362	ShopDWG Appovalfor Basketball Court Making	1.00	100%	100%	13 Jun 26	13Jun-26	13 Jun 26 A	13Jun-26A	$000	$000	$0.00	0.00
MLTX02-004EN-363	ShopDWG Appovalfor Padel Cart Stucture	1.00	100%	100%	13 Jun 26	13Jun-26	13 Jun 26 A	13Jun-26A	$000	$000	$0.00	0.00
MECHANCALWORKS		1.00	0%	0%	07 May-26	07May-26	07 May 26 A	07May-26A	$000	$000	$0.00	0.00
MLTX02-004EN-365	ShopDWG Appovalfor HVACPlan	1.00	100%	100%	07 May-26	07May-26	07 May 26 A	07May-26A	$000	$000	$0.00	0.00
MLTX02-004EN-366	ShopDWG Appovalfor ExhaustAir Plan	1.00	100%	100%	07 May-26	07May-26	07 May 26 A	07May-26A	$000	$000	$0.00	0.00
ELECTRCALWORKS		12200	0%	0%	15 Apr 26	11Jul-26	15 Apr 26 A	26Aug-26A	$000	$000	$0.00	-4000
MLTX02-004EN-368	ShopDWG Appovalfor Lighting Layout	1000	100%	100%	15 Apr 26	26Apr-26	15 Apr 26 A	26Apr-26A	$000	$000	$0.00	0.00
MLTX02-004EN-369	ShopDWG Appovalfor Power Layout	1000	100%	100%	15 Apr 26	26Apr-26	15 Apr 26 A	26Apr-26A	$000	$000	$0.00	0.00
MLTX02-004EN-373	ShopDWG Appovalfor Power Single line Diagram	6.00	100%	100%	05 Jul-26	11Jul-26	11 Jul-26A	11Jul-26A	$000	$000	$0.00	5.00
MLTX02-004EN-374	ShopDWG Appovalfor Panel Board Schedules	6.00	100%	100%	05 Jul-26	11Jul-26	11 Jul-26A	11Jul-26A	$000	$000	$0.00	5.00
MLTX02-004EN-370	ShopDWG Appovalfor Power InstallationDetails	1000	100%	100%	15 Apr 26	26Apr-26	15 Apr 26 A	26Apr-26A	$000	$000	$0.00	0.00
MLTX02-004EN-376	ShopDWG Appovalfor CCTV Details	6.00	100%	100%	05 Jul-26	11Jul-26	26 Aug 26 A	26Aug-26A	$000	$000	$0.00	5.00
MLTX02-004EN-377	ShopDWG Appovalfor CCTV Layout	6.00	100%	100%	05 Jul-26	11Jul-26	26 Aug 26 A	26Aug-26A	$000	$000	$0.00	5.00

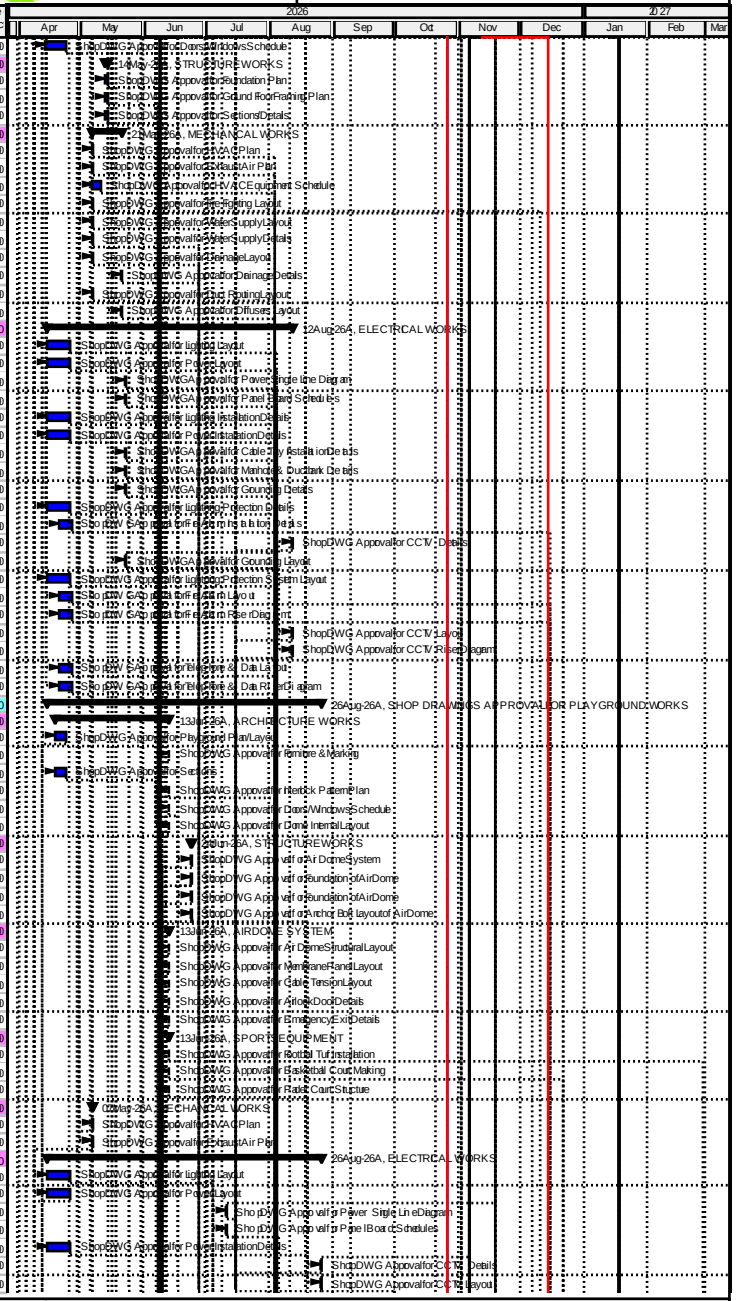


© Oracle Corporation

ActivityID	ActivityName	Orginal Duration	Schedule %	Performance% Complete	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Variance - BL Project
MLTX02-004EN-378	ShopDWG Appovalfor CCTV RiserDiagram	6.00	100%	100%	05 Jul-25	11Jul-26	26 Aug 25 A	26Aug-26A	$000	$000	$0.00	5.00
SHOP DRAWIN GSAPPROVALFOR LANDSCAPE WORKS		6200	0%	0%	11 Apr 26	24Jun-26	11 Apr 26 A	24Jun-26A	$000	$000	$0.00	0.00
ARCHITECTURE WORKS		2300	0%	0%	19 Apr 26	14May-26	19 Apr 26 A	14May-26A	$000	$000	$0.00	0.00
MLTX02-004EN-381	ShopDWG Appovalfor landscape Layout	5.00	100%	100%	19 Apr 26	23Apr-26	19 Apr 26 A	24Apr-26A	$000	$000	$0.00	0.00
MLTX02-004EN-382	ShopDWG Appovalfor Hardscape Plan	2.00	100%	100%	13 May-26	14May-26	13 May 26 A	14May-26A	$000	$000	$0.00	0.00
MLTX02-004EN-383	ShopDWG Appovalfor Planting Plan	2.00	100%	100%	13 May-26	14May-26	13 May 26 A	14May-26A	$000	$000	$0.00	0.00
MLTX02-004EN-384	ShopDWG Appovalfor landscape Details	2.00	100%	100%	13 May-26	14May-26	13 May 26 A	14May-26A	$000	$000	$0.00	0.00
MECHANCAL WORKS		1.00	0%	0%	24 Jun 26	24Jun-26	24 Jun 26 A	24Jun-26A	$000	$000	$0.00	0.00
MLTX02-004EN-388	ShopDWG Appovalfor IrrigationDetails	1.00	100%	100%	24 Jun 26	24Jun-26	24 Jun 26 A	24Jun-26A	$000	$000	$0.00	0.00
MLTX02-004EN-392	ShopDWG Appovalfor IrrigationLayout	1.00	100%	100%	24 Jun 26	24Jun-26	24 Jun 26 A	24Jun-26A	$000	$000	$0.00	0.00
ELECTRCAL WORKS		3700	0%	0%	11 Apr 26	23May-26	11 Apr 26 A	23May-26A	$000	$000	$0.00	0.00
MLTX02-004EN-397	ShopDWG Appovalfor lighting General Arrangement	1000	100%	100%	11 Apr 26	21Apr-26	11 Apr 26 A	21Apr-26A	$000	$000	$0.00	0.00
MLTX02-004EN-398	ShopDWG Appovalfor lighting Network Layout	1000	100%	100%	11 Apr 26	21Apr-26	11 Apr 26 A	21Apr-26A	$000	$000	$0.00	0.00
MLTX02-004EN-399	ShopDWG Appovalfor lighting Details	1000	100%	100%	11 Apr 26	21Apr-26	11 Apr 26 A	21Apr-26A	$000	$000	$0.00	0.00
MLTX02-004EN-396	ShopDWG Appovalfor lighting Simple Line Diagram	1.00	100%	100%	23 May-26	23May-26	23 May 26 A	23May-26A	$000	$000	$0.00	0.00
METHOD STATEMENTS		19200	0%	0%	31 Mar 26	03Aug-26	31 Mar 26 A	14Nov-26	$000	$000	$0.00	-8700
METHOD STATEMENT SUBMITTAL		18200	0%	0%	31 Mar 26	19Jul-26	31 Mar 26 A	02Nov-26	$000	$000	$0.00	-9000
CIVL WORKS		4500	0%	0%	31 Mar 26	21May-26	31 Mar 26 A	21May-26A	$000	$000	$0.00	0.00
MLTX02-004EN-4020	Preparation & Submissionof MethodStatement forEarthwork	1700	100%	100%	31 Mar 26	19Apr-26	31 Mar 26 A	19Apr-26A	$000	$000	$0.00	0.00
MLTX02-004EN-4030	Preparation & Submissionof MethodStatement forConcrete Works	1.00	100%	100%	21 May-26	21May-26	21 May 26 A	21May-26A	$000	$000	$0.00	0.00
MLTX02-004EN-4040	Preparation & Submissionof MethodStatement forWaterproding	2200	100%	100%	31 Mar 26	25Apr-26	31 Mar 26 A	25Apr-26A	$000	$000	$0.00	0.00
ARCHITECTURE WORKS		13300	0%	0%	31 May-26	11Jul-26	31 May 26 A	02Nov-26	$000	$000	$0.00	-9700
MLTX02-004EN-4140	Preparation & Submissionof MethodStatement forFenceWorks	6.00	100%	0%	05 Jul-25	11Jul-26	27 Oct 26	02Nov-26	$000	$000	$0.00	0.00
MLTX02-004EN-4060	Preparation & Submissionof MethodStatement forPlastteringWorks	1.00	100%	100%	18 Jun 26	18Jun-26	18 Jun 26 A	18Jun-26A	$000	$000	$0.00	0.00
MLTX02-004EN-4070	Preparation & Submissionof MethodStatement forMasonay Works	1.00	100%	100%	18 Jun 26	18Jun-26	18 Jun 26 A	18Jun-26A	$000	$000	$0.00	0.00
MLTX02-004EN-4080	Preparation & Submissionof MethodStatement forTilingWorks	1.00	100%	100%	06 Jun 26	06Jun-26	06 Jun 26 A	06Jun-26A	$000	$000	$0.00	0.00
MLTX02-004EN-4090	Preparation & Submissionof MethodStatement forSeatsBenchesWoks	1.00	100%	100%	18 Jun 26	18Jun-26	18 Jun 26 A	18Jun-26A	$000	$000	$0.00	0.00
MLTX02-004EN-4100	Preparation & Submissionof MethodStatement forDoorsWindows Woks	1.00	100%	100%	06 Jun 26	06Jun-26	06 Jun 26 A	06Jun-26A	$000	$000	$0.00	0.00
MLTX02-004EN-4110	Preparation & Submissionof MethodStatement forInterlock/Curbstone Works	1.00	100%	100%	31 May-26	31May-26	31 May 26 A	31May-26A	$000	$000	$0.00	0.00
MLTX02-004EN-4120	Preparation & Submissionof MethodStatement forParking Woks	1.00	100%	100%	31 May-26	31May-26	31 May 26 A	31May-26A	$000	$000	$0.00	0.00
MLTX02-004EN-4130	Preparation & Submissionof MethodStatement forSoftScapeWorks	6.00	100%	100%	05 Jul-25	11Jul-26	11 Jul-26A	11Jul-26A	$000	$000	$0.00	5.00
MLTX02-004EN-4150	Preparation & Submissionof MethodStatement forAirDome Woks	6.00	100%	100%	05 Jul-25	11Jul-26	17 Aug 25 A	17Aug-26A	$000	$000	$0.00	5.00
MLTX02-004EN-4160	Preparation & Submissionof MethodStatement forMetalWoks	6.00	100%	100%	05 Jul-25	11Jul-26	11 Jul-26A	11Jul-26A	$000	$000	$0.00	5.00
MLTX02-004EN-4170	Preparation & Submissionof MethodStatement forPartitions Woks	6.00	100%	100%	05 Jul-25	11Jul-26	15 Jul-26A	15Jul-26A	$000	$000	$0.00	5.00
MLTX02-004EN-4180	Preparation & Submissionof MethodStatement forGypsumBoardWorks	1.00	100%	100%	13 Jun 26	13Jun-26	13 Jun 26 A	13Jun-26A	$000	$000	$0.00	0.00
MECHANICALWORKS		4800	0%	0%	07 Apr 26	04Jun-26	07 Apr 26 A	04Jun-26A	$000	$000	$0.00	0.00
MLTX02-004EN-4200	Preparation & Submissionof MethodStatement forSewageDrainage System	1.00	100%	100%	31 May-26	31May-26	31 May 26 A	31May-26A	$000	$000	$0.00	0.00
MLTX02-004EN-4210	Preparation & Submissionof MethodStatement forWater Supply System	1.00	100%	100%	04 Jun 26	04Jun-26	04 Jun 26 A	04Jun-26A	$000	$000	$0.00	0.00
MLTX02-004EN-4220	Preparation & Submissionof MethodStatement forFire FightingSystem	7.00	100%	100%	07 Apr 26	14Apr-26	07 Apr 26 A	14Apr-26A	$000	$000	$0.00	0.00
MLTX02-004EN-4230	Preparation & Submissionof MethodStatement forIrrigation System	1.00	100%	100%	04 Jun 26	04Jun-26	04 Jun 26 A	04Jun-26A	$000	$000	$0.00	0.00
MLTX02-004EN-4240	Preparation & Submissionof MethodStatement forHVAC System	1.00	100%	100%	04 Jun 26	04Jun-26	04 Jun 26 A	04Jun-26A	$000	$000	$0.00	0.00
ELECTRCAL WORKS		5800	0%	0%	18 Jun 26	19Jul-26	18 Jun 26 A	11Aug-26A	$000	$000	$0.00	-2000
MLTX02-004EN-4310	Preparation & Submissionof MethodStatement forElecticalConduits/PullingWorks	1.00	100%	100%	18 Jun 26	18Jun-26	18 Jun 26 A	18Jun-26A	$000	$000	$0.00	0.00
MLTX02-004EN-4330	Preparation & Submissionof MethodStatement forLightingPoles Installation	1.00	100%	100%	18 Jun 26	18Jun-26	18 Jun 26 A	18Jun-26A	$000	$000	$0.00	0.00
MLTX02-004EN-4260	Preparation & Submissionof MethodStatement forTelecommunication& DataSyste	7.00	100%	100%	12 Jul-25	19Jul-26	15 Jul-26A	15Jul-26A	$000	$000	$0.00	6.00
MLTX02-004EN-4270	Preparation & Submissionof MethodStatement forCCTV System	7.00	100%	100%	12 Jul-25	19Jul-26	22 Jul-26A	22Jul-26A	$000	$000	$0.00	6.00
MLTX02-004EN-4280	Preparation & Submissionof MethodStatement forLightingWorks	1.00	100%	100%	18 Jun 26	18Jun-26	18 Jun 26 A	18Jun-26A	$000	$000	$0.00	0.00
MLTX02-004EN-4290	Preparation & Submissionof MethodStatement forEarthing/Lightning Works	1.00	100%	100%	18 Jun 26	18Jun-26	18 Jun 26 A	18Jun-26A	$000	$000	$0.00	0.00
MLTX02-004EN-4300	Preparation & Submissionof MethodStatement forPanelBoardsWoks	6.00	100%	100%	05 Jul-25	11Jul-26	11 Aug 25 A	11Aug-26A	$000	$000	$0.00	5.00
METHOD STATEMENT APPROVAL		17900	0%	0%	15 Apr 26	03Aug-26	15 Apr 26 A	14Nov-26	$000	$000	$0.00	-8700
CIVL WORKS		1.00	0%	0%	31 May-26	31May-26	31 May 26 A	31May-26A	$000	$000	$0.00	0.00
MLTX02-004EN-4360	Appoval d Method Statementfor Earthwok	1.00	100%	100%	31 May-26	31May-26	31 May 26 A	31May-26A	$000	$000	$0.00	0.00
MLTX02-004EN-4370	Appoval d Method Statementfor Concrete Woks	1.00	100%	100%	31 May-26	31May-26	31 May 26 A	31May-26A	$000	$000	$0.00	0.00
MLTX02-004EN-4380	Appoval d Method Statementfor Wateproofing	1.00	100%	100%	31 May-26	31May-26	31 May 26 A	31May-26A	$000	$000	$0.00	0.00
ARCHITECTURE WORKS		14300	0%	0%	31 May-26	22Jul-26	31 May 26 A	14Nov-26	$000	$000	$0.00	-9700
MLTX02-004EN-4480	Appoval d Method Statementfor fence Works	1000	100%	0%	12 Jul-25	22Jul-26	03 Nov 26	14Nov-26	$000	$000	$0.00	0.00
MLTX02-004EN-4400	Appoval d Method Statementfor Plasteing Works	1.00	100%	100%	16 Jun 26	16Jun-26	16 Jun 26 A	16Jun-26A	$000	$000	$0.00	0.00
MLTX02-004EN-4410	Appoval d Method Statementfor MasonaryWorks	1.00	100%	100%	16 Jun 26	16Jun-26	16 Jun 26 A	16Jun-26A	$000	$000	$0.00	0.00
MLTX02-004EN-4420	Appoval d Method Statementfor Tiling Woks	1.00	100%	100%	06 Jun 26	06Jun-26	06 Jun 26 A	06Jun-26A	$000	$000	$0.00	0.00
MLTX02-004EN-4430	Appoval d Method Statementfor Seats/Benches Works	6.00	100%	100%	05 Jul-25	11Jul-26	11 Jul-26A	11Jul-26A	$000	$000	$0.00	5.00
MLTX02-004EN-4440	Appoval d Method Statementfor Doors/WindowsWorks	1.00	100%	100%	06 Jun 26	06Jun-26	06 Jun 26 A	06Jun-26A	$000	$000	$0.00	0.00
MLTX02-004EN-4450	Appoval d Method Statementfor Intelock/Cubstone Woks	1.00	100%	100%	31 May-26	31May-26	31 May 26 A	31May-26A	$000	$000	$0.00	0.00
MLTX02-004EN-4460	Appoval d Method Statementfor ParkingWorks	1.00	100%	100%	31 May-26	31May-26	31 May 26 A	31May-26A	$000	$000	$0.00	0.00
MLTX02-004EN-4470	Appoval d Method Statementfor Soft Scape Woks	1000	100%	100%	12 Jul-25	22Jul-26	11 Jul-26A	11Jul-26A	$000	$000	$0.00	9.00
MLTX02-004EN-4490	Appoval d Method Statementfor Air DomeWorks	1000	100%	100%	12 Jul-25	22Jul-26	27 Aug 25 A	27Aug-26A	$000	$000	$0.00	9.00
MLTX02-004EN-4510	Appoval d Method Statementfor PartitonsWorks	1000	100%	100%	12 Jul-25	22Jul-26	27 Aug 25 A	27Aug-26A	$000	$000	$0.00	9.00
MLTX02-004EN-4520	Appoval d Method Statementfor Gypsum Board Woks	1.00	100%	100%	18 Jun 26	18Jun-26	18 Jun 26 A	18Jun-26A	$000	$000	$0.00	0.00
MECHANICALWORKS		4700	0%	0%	15 Apr 26	11Jun-26	15 Apr 26 A	11Jun-26A	$000	$000	$0.00	0.00
MLTX02-004EN-4540	Appoval d Method Statementfor Sewage/DainageSystem	1.00	100%	100%	11 Jun 26	11Jun-26	11 Jun 26 A	11Jun-26A	$000	$000	$0.00	0.00
MLTX02-004EN-4550	Appoval d Method Statementfor WaterSupplySystem	1.00	100%	100%	11 Jun 26	11Jun-26	11 Jun 26 A	11Jun-26A	$000	$000	$0.00	0.00
MLTX02-004EN-4560	Appoval d Method Statementfor fireFighting System	1000	100%	100%	15 Apr 26	26Apr-26	15 Apr 26 A	26Apr-26A	$000	$000	$0.00	0.00

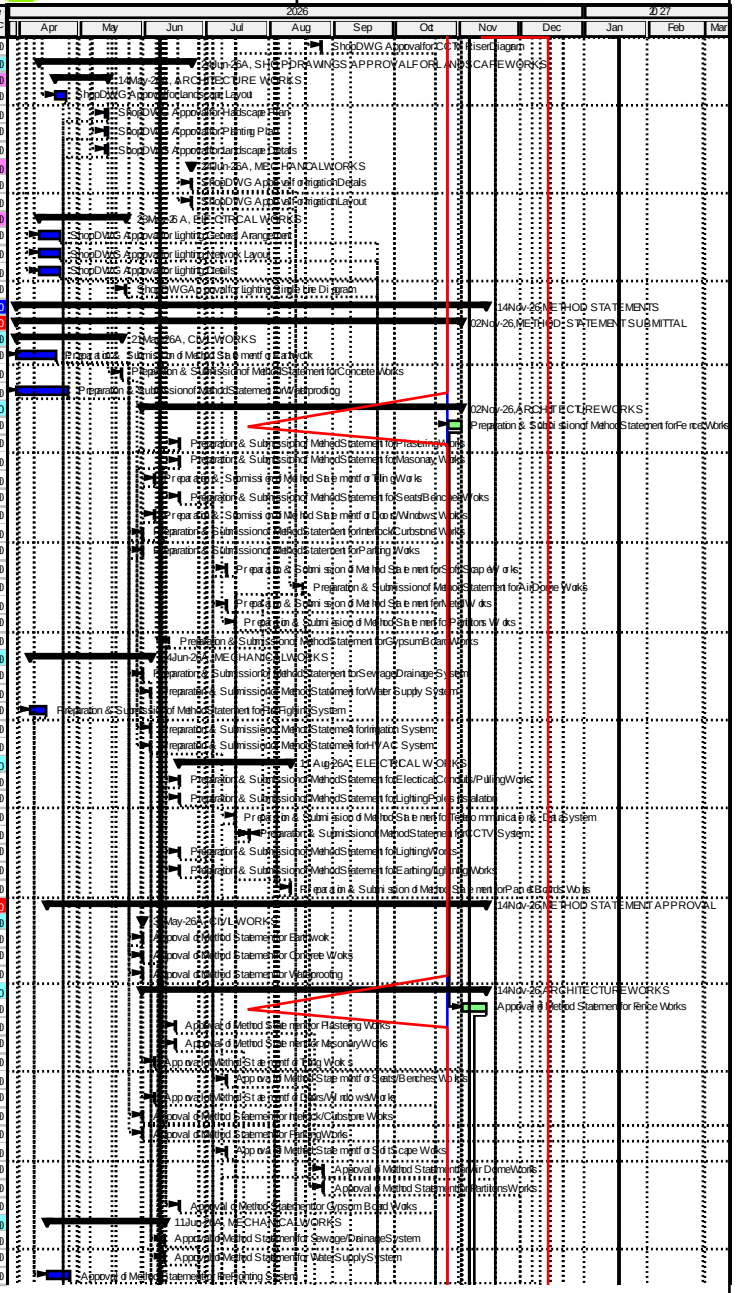


© Oracle Corporation

ActivityID	ActivityName	Orginal Duration	Schedule %	Performance% Complete	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Variance - BL Project
MLTX02004EN-4570	Approval of Method Statement for Irigation System	1.00	100%	100%	11-Jun-26	11-Jun-26	11-Jun-26A	11-Jun-26A	$000	$000	$0.00	0.00
MLTX02004EN-4580	Approval of Method Statement for HVAC System	1.00	100%	100%	11-Jun-26	11-Jun-26	11-Jun-26A	11-Jun-26A	$000	$000	$0.00	0.00
ELECTRICAL WORKS		70.00	0%	0%	16-Jun-26	03-Aug-26	16-Jun-26A	12-Aug-26A	$000	$000	$0.00	-800
MLTX02004EN-4600	Approval of Method Statement for Electrical Conduits/Pulling Works	1.00	100%	100%	16-Jun-26	16-Jun-26	16-Jun-26A	16-Jun-26A	$000	$000	$0.00	0.00
MLTX02004EN-4620	Approval of Method Statement for Lighting Poles Installation	10.00	100%	100%	05-Jul-26	15-Jul-26	11-Jul-26A	11-Jul-26A	$000	$000	$0.00	9.00
MLTX02004EN-4630	Approval of Method Statement for Telecommunication & Data System	10.00	100%	100%	23-Jul-26	03-Aug-26	15-Jul-26A	15-Jul-26A	$000	$000	$0.00	9.00
MLTX02004EN-4640	Approval of Method Statement for CCTV System	10.00	100%	100%	23-Jul-26	03-Aug-26	22-Jul-26A	22-Jul-26A	$000	$000	$0.00	9.00
MLTX02004EN-4650	Approval of Method Statement for Lighting Works	10.00	100%	100%	05-Jul-26	15-Jul-26	11-Jul-26A	11-Jul-26A	$000	$000	$0.00	9.00
MLTX02004EN-4660	Approval of Method Statement for Earthing/Lightning Works	10.00	100%	100%	05-Jul-26	15-Jul-26	11-Jul-26A	11-Jul-26A	$000	$000	$0.00	9.00
MLTX02004EN-4670	Approval of Method Statement for Panel Boards Works	10.00	100%	100%	12-Jul-26	22-Jul-26	12-Aug-26A	12-Aug-26A	$000	$000	$0.00	9.00
PRE-QUALIFICATION& MATERIAL		212.00	0%	0%	31-Mar-26	02-Sep-26	31-Mar-26A	07-Dec-26	$000	$000	$0.00	-8100
PRE-QUALIFICATION		45.00	0%	0%	31-Mar-26	21-May-26	31-Mar-26A	21-May-26A	$000	$000	$0.00	0.00
TOILETSERVICE WORKS		21.00	0%	0%	31-Mar-26	23-Apr-26	31-Mar-26A	23-Apr-26A	$000	$000	$0.00	0.00
STEEL REINFORCEMENT		12.00	0%	0%	31-Mar-26	13-Apr-26	31-Mar-26A	13-Apr-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-472	PreQualification Submittal for Steel Reinforcement	11.00	100%	100%	31-Mar-26	12-Apr-26	31-Mar-26A	12-Apr-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-473	PreQualification Approval for Steel Reinforcement	2.00	100%	100%	12-Apr-26	13-Apr-26	12-Apr-26A	13-Apr-26A	$000	$000	$0.00	0.00
READY MIX CONCRETE		21.00	0%	0%	31-Mar-26	23-Apr-26	31-Mar-26A	23-Apr-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-475	PreQualification Submittal for Ready Mixed Concrete	11.00	100%	100%	31-Mar-26	12-Apr-26	31-Mar-26A	12-Apr-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-476	PreQualification Approval of Ready Mixed Concrete	11.00	100%	100%	12-Apr-26	23-Apr-26	12-Apr-26A	23-Apr-26A	$000	$000	$0.00	0.00
CONCRETE BLOCKS		21.00	0%	0%	31-Mar-26	23-Apr-26	31-Mar-26A	23-Apr-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-478	PreQualification Submittal for Concrete Blocks	11.00	100%	100%	31-Mar-26	12-Apr-26	31-Mar-26A	12-Apr-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-479	PreQualification Approval for Concrete Blocks	15.00	100%	100%	07-Apr-26	23-Apr-26	07-Apr-26A	23-Apr-26A	$000	$000	$0.00	0.00
WATERPROOFING		12.00	0%	0%	31-Mar-26	13-Apr-26	31-Mar-26A	13-Apr-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-481	PreQualification Submittal for Water Proofing	10.00	100%	100%	31-Mar-26	11-Apr-26	31-Mar-26A	11-Apr-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-482	PreQualification Approval for Water Proofing	3.00	100%	100%	11-Apr-26	13-Apr-26	11-Apr-26A	13-Apr-26A	$000	$000	$0.00	0.00
FLOOR/WALL TILES		11.00	0%	0%	31-Mar-26	12-Apr-26	31-Mar-26A	12-Apr-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-484	PreQualification Submittal for Tiling Materials	10.00	100%	100%	31-Mar-26	11-Apr-26	31-Mar-26A	11-Apr-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-485	PreQualification Approval for Tailing Material	2.00	100%	100%	11-Apr-26	12-Apr-26	11-Apr-26A	12-Apr-26A	$000	$000	$0.00	0.00
SUSPENDED CEILING		12.00	0%	0%	31-Mar-26	13-Apr-26	31-Mar-26A	13-Apr-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-487	PreQualification Submittal for Suspend Ceiling	11.00	100%	100%	31-Mar-26	12-Apr-26	31-Mar-26A	12-Apr-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-488	PreQualification Approval for Suspend Ceiling	2.00	100%	100%	12-Apr-26	13-Apr-26	12-Apr-26A	13-Apr-26A	$000	$000	$0.00	0.00
DOORS/WINDOWS		11.00	0%	0%	31-Mar-26	12-Apr-26	31-Mar-26A	12-Apr-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-490	PreQualification Submittal for Doors/Windows	10.00	100%	100%	31-Mar-26	11-Apr-26	31-Mar-26A	11-Apr-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-491	PreQualification Approval for Doors/Windows	2.00	100%	100%	11-Apr-26	12-Apr-26	11-Apr-26A	12-Apr-26A	$000	$000	$0.00	0.00
FURNITURES		11.00	0%	0%	31-Mar-26	12-Apr-26	31-Mar-26A	12-Apr-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-493	PreQualification Submittal for Furnitures	10.00	100%	100%	31-Mar-26	11-Apr-26	31-Mar-26A	11-Apr-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-494	PreQualification Approval for Furnitures	2.00	100%	100%	11-Apr-26	12-Apr-26	11-Apr-26A	12-Apr-26A	$000	$000	$0.00	0.00
SANITARY FIXTURES		11.00	0%	0%	31-Mar-26	12-Apr-26	31-Mar-26A	12-Apr-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-496	PreQualification Submittal for Sanitary Fixtures	10.00	100%	100%	31-Mar-26	11-Apr-26	31-Mar-26A	11-Apr-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-497	PreQualification Approval for Sanitay Fixtures	2.00	100%	100%	11-Apr-26	12-Apr-26	11-Apr-26A	12-Apr-26A	$000	$000	$0.00	0.00
WATER SUPPLY PIPES		11.00	0%	0%	31-Mar-26	12-Apr-26	31-Mar-26A	12-Apr-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-499	PreQualification Submittal for Water Supply Pipes	10.00	100%	100%	31-Mar-26	11-Apr-26	31-Mar-26A	11-Apr-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-500	PreQualification Approval for Water Supply Pipes	2.00	100%	100%	11-Apr-26	12-Apr-26	11-Apr-26A	12-Apr-26A	$000	$000	$0.00	0.00
SEWAGE DRAINAGE PIPES		11.00	0%	0%	31-Mar-26	12-Apr-26	31-Mar-26A	12-Apr-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-502	PreQualification Submittal for Sewage Drainage Pipes	10.00	100%	100%	31-Mar-26	11-Apr-26	31-Mar-26A	11-Apr-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-503	PreQualification Approval for Sewage/Drainage Pipes	2.00	100%	100%	11-Apr-26	12-Apr-26	11-Apr-26A	12-Apr-26A	$000	$000	$0.00	0.00
PACKAGE ACUNITS		8.00	0%	0%	07-Apr-26	15-Apr-26	07-Apr-26A	15-Apr-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-505	PreQualification Submittal for Package AC Units	6.00	100%	100%	07-Apr-26	13-Apr-26	07-Apr-26A	13-Apr-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-506	PreQualification Approval for Package AC Units	5.00	100%	100%	11-Apr-26	15-Apr-26	11-Apr-26A	15-Apr-26A	$000	$000	$0.00	0.00
AIRDIFFUSSERS/GRILLS		8.00	0%	0%	07-Apr-26	15-Apr-26	07-Apr-26A	15-Apr-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-508	PreQualification Submittal for Air Diffusers/Grills	6.00	100%	100%	07-Apr-26	13-Apr-26	07-Apr-26A	13-Apr-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-509	PreQualification Approval for Air Diffusers/Grills	5.00	100%	100%	11-Apr-26	15-Apr-26	11-Apr-26A	15-Apr-26A	$000	$000	$0.00	0.00
GALVANIZED DUCTS		8.00	0%	0%	07-Apr-26	15-Apr-26	07-Apr-26A	15-Apr-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-511	PreQualification Submittal for Galvanized Ducts	6.00	100%	100%	07-Apr-26	13-Apr-26	07-Apr-26A	13-Apr-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-512	PreQualification Approval for Galvanized Ducts	5.00	100%	100%	11-Apr-26	15-Apr-26	11-Apr-26A	15-Apr-26A	$000	$000	$0.00	0.00
EXHAUST FANS		8.00	0%	0%	07-Apr-26	15-Apr-26	07-Apr-26A	15-Apr-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-514	PreQualification Submittal for Exhaust Fans	5.00	100%	100%	07-Apr-26	12-Apr-26	07-Apr-26A	12-Apr-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-515	PreQualification Approval for Exhaust Fans	5.00	100%	100%	11-Apr-26	15-Apr-26	11-Apr-26A	15-Apr-26A	$000	$000	$0.00	0.00
LIGHTING FIXTURES		8.00	0%	0%	07-Apr-26	15-Apr-26	07-Apr-26A	15-Apr-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-517	PreQualification Submittal for Lighting Fixtures	3.00	100%	100%	07-Apr-26	09-Apr-26	07-Apr-26A	09-Apr-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-518	PreQualification Approval for Lighting Fixtures	5.00	100%	100%	11-Apr-26	15-Apr-26	11-Apr-26A	15-Apr-26A	$000	$000	$0.00	0.00
SWITCHES/SOCKETS		8.00	0%	0%	07-Apr-26	15-Apr-26	07-Apr-26A	15-Apr-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-520	PreQualification Submittal for Switches/Sockets	3.00	100%	100%	07-Apr-26	09-Apr-26	07-Apr-26A	09-Apr-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-521	PreQualification Approval for Switches/Sockets	5.00	100%	100%	11-Apr-26	15-Apr-26	11-Apr-26A	15-Apr-26A	$000	$000	$0.00	0.00
EARTHING SYSTEM		8.00	0%	0%	07-Apr-26	15-Apr-26	07-Apr-26A	15-Apr-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-523	PreQualification Submittal for Earthing System	3.00	100%	100%	07-Apr-26	09-Apr-26	07-Apr-26A	09-Apr-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-524	PreQualification Approval for Eathing System	5.00	100%	100%	11-Apr-26	15-Apr-26	11-Apr-26A	15-Apr-26A	$000	$000	$0.00	0.00
DISTRIBUTION PANNELS		8.00	0%	0%	07-Apr-26	15-Apr-26	07-Apr-26A	15-Apr-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-526	PreQualification Submittal for Distribution Panels	3.00	100%	100%	07-Apr-26	09-Apr-26	07-Apr-26A	09-Apr-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-527	PreQualification Approval for Distribution Panels	5.00	100%	100%	11-Apr-26	15-Apr-26	11-Apr-26A	15-Apr-26A	$000	$000	$0.00	0.00
PLAYGROUND WORKS		21.00	0%	0%	31-Mar-26	23-Apr-26	31-Mar-26A	23-Apr-26A	$000	$000	$0.00	0.00
PVC MEMBRANE		14.00	0%	0%	31-Mar-26	15-Apr-26	31-Mar-26A	15-Apr-26A	$000	$000	$0.00	0.00

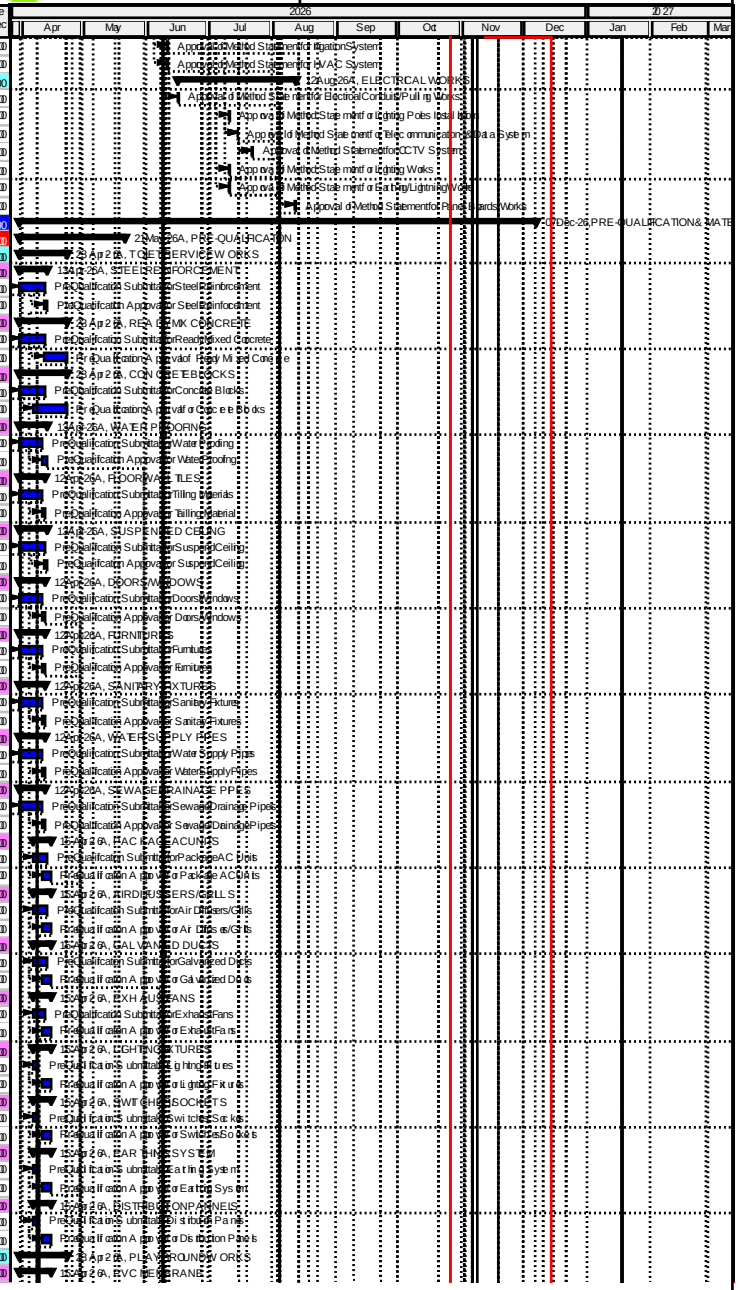


© Oracle Corporation

ActivityID	ActivityName	Orginal Duration	Schedule %	Performance% Complete	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Variance - BL Project
MLTX02-004EN-530	PreQualifcation SubmittalforPVC Membane	1100	100%	100%	31 Mar 26	12Apr-26	31 Mar 26A	12Apr-26A	$000	$000	$0.00	0.00
MLTX02-004EN-531	PreQualifcation Appovalfor PVCMembrane	4.00	100%	100%	12 Apr 26	15Apr-26	12 Apr 26A	15Apr-26A	$000	$000	$0.00	0.00
STEELTENSION CABLES		1400	0%	0%	31 Mar 26	15Apr-26	31 Mar 26A	15Apr-26A	$000	$000	$0.00	0.00
MLTX02-004EN-532	PreQualifcation SubmittalforSteelTension Cables	1200	100%	100%	31 Mar 26	13Apr-26	31 Mar 26A	13Apr-26A	$000	$000	$0.00	0.00
MLTX02-004EN-534	PreQualifcation Appovalfor SteelTensionCables	3.00	100%	100%	13 Apr 26	15Apr-26	13 Apr 26A	15Apr-26A	$000	$000	$0.00	0.00
EMERGENCY DOORS		1400	0%	0%	31 Mar 26	15Apr-26	31 Mar 26A	15Apr-26A	$000	$000	$0.00	0.00
MLTX02-004EN-536	PreQualifcation SubmittalforEmergency Doors	1200	100%	100%	31 Mar 26	13Apr-26	31 Mar 26A	13Apr-26A	$000	$000	$0.00	0.00
MLTX02-004EN-537	PreQualifcation Appovalfor EmergencyDoors	3.00	100%	100%	13 Apr 26	15Apr-26	13 Apr 26A	15Apr-26A	$000	$000	$0.00	0.00
PRESSURE UNITS		1400	0%	0%	31 Mar 26	15Apr-26	31 Mar 26A	15Apr-26A	$000	$000	$0.00	0.00
MLTX02-004EN-538	PreQualifcation SubmittalforPressure Units	1200	100%	100%	31 Mar 26	13Apr-26	31 Mar 26A	13Apr-26A	$000	$000	$0.00	0.00
MLTX02-004EN-540	PreQualifcation Appovalfor Pessure Units	3.00	100%	100%	13 Apr 26	15Apr-26	13 Apr 26A	15Apr-26A	$000	$000	$0.00	0.00
AIRLOCK DOORS		1400	0%	0%	31 Mar 26	15Apr-26	31 Mar 26A	15Apr-26A	$000	$000	$0.00	0.00
MLTX02-004EN-542	PreQualifcation SubmittalforLockDoors	1200	100%	100%	31 Mar 26	13Apr-26	31 Mar 26A	13Apr-26A	$000	$000	$0.00	0.00
MLTX02-004EN-543	PreQualifcation Appovalfor lock Doos	3.00	100%	100%	13 Apr 26	15Apr-26	13 Apr 26A	15Apr-26A	$000	$000	$0.00	0.00
ARTIFICIAL TURF		1100	0%	0%	31 Mar 26	12Apr-26	31 Mar 26A	12Apr-26A	$000	$000	$0.00	0.00
MLTX02-004EN-545	PreQualifcation SubmittalforArtificial TURF	1000	100%	100%	31 Mar 26	11Apr-26	31 Mar 26A	11Apr-26A	$000	$000	$0.00	0.00
MLTX02-004EN-546	PreQualifcation Appovalfor ArtificialTURF	2.00	100%	100%	11 Apr 26	12Apr-26	11 Apr 26A	12Apr-26A	$000	$000	$0.00	0.00
RUBBER GRANULES		1400	0%	0%	31 Mar 26	15Apr-26	31 Mar 26A	15Apr-26A	$000	$000	$0.00	0.00
MLTX02-004EN-548	PreQualifcation SubmittalforRubberGranules	1200	100%	100%	31 Mar 26	13Apr-26	31 Mar 26A	13Apr-26A	$000	$000	$0.00	0.00
MLTX02-004EN-549	PreQualifcation Appovalfor RubberGranules	3.00	100%	100%	13 Apr 26	15Apr-26	13 Apr 26A	15Apr-26A	$000	$000	$0.00	0.00
PADEL GIASS		1400	0%	0%	31 Mar 26	15Apr-26	31 Mar 26A	15Apr-26A	$000	$000	$0.00	0.00
MLTX02-004EN-551	PreQualifcation SubmittalforPadelGlass	1200	100%	100%	31 Mar 26	13Apr-26	31 Mar 26A	13Apr-26A	$000	$000	$0.00	0.00
MLTX02-004EN-552	PreQualifcation Appovalfor Padel Glss	3.00	100%	100%	13 Apr 26	15Apr-26	13 Apr 26A	15Apr-26A	$000	$000	$0.00	0.00
PADEL WIREMESH/STEEL SETS		1400	0%	0%	31 Mar 26	15Apr-26	31 Mar 26A	15Apr-26A	$000	$000	$0.00	0.00
MLTX02-004EN-554	PreQualifcation SubmittalforWireMeshSteelSets	1200	100%	100%	31 Mar 26	13Apr-26	31 Mar 26A	13Apr-26A	$000	$000	$0.00	0.00
MLTX02-004EN-555	PreQualifcation Appovalfor WireMesh/Steel Sets	3.00	100%	100%	13 Apr 26	15Apr-26	13 Apr 26A	15Apr-26A	$000	$000	$0.00	0.00
AGGREGATE BASECOURSE		1400	0%	0%	31 Mar 26	15Apr-26	31 Mar 26A	15Apr-26A	$000	$000	$0.00	0.00
MLTX02-004EN-557	PreQualifcation SubmittalforAggregate Base Course	1400	100%	100%	31 Mar 26	15Apr-26	31 Mar 26A	15Apr-26A	$000	$000	$0.00	0.00
MLTX02-004EN-558	PreQualifcation Appovalfor Aggregate BaseCourse	1.00	100%	100%	15 Apr 26	15Apr-26	15 Apr 26A	15Apr-26A	$000	$000	$0.00	0.00
BITUMNOUS BASE &WEARING COURSE		7.00	0%	0%	07 Apr 26	14Apr-26	07 Apr 26A	14Apr-26A	$000	$000	$0.00	0.00
MLTX02-004EN-560	PreQualifcation SubmittalforBituminous Base & WearingCource	5.00	100%	100%	07 Apr 26	12Apr-26	07 Apr 26A	12Apr-26A	$000	$000	$0.00	0.00
MLTX02-004EN-561	PreQualifcation Appovalfor he Site	3.00	100%	100%	12 Apr 26	14Apr-26	12 Apr 26A	14Apr-26A	$000	$000	$0.00	0.00
INTERLOCKNG PAVING		1500	0%	0%	07 Apr 26	23Apr-26	07 Apr 26A	23Apr-26A	$000	$000	$0.00	0.00
MLTX02-004EN-563	PreQualifcation SubmittalforInterlocking Block Paves	5.00	100%	100%	07 Apr 26	12Apr-26	07 Apr 26A	12Apr-26A	$000	$000	$0.00	0.00
MLTX02-004EN-564	PreQualifcation Appovalfor Interbcking BlockPavers	1100	100%	100%	12 Apr 26	23Apr-26	12 Apr 26A	23Apr-26A	$000	$000	$0.00	0.00
MARKINGPAINT		8.00	0%	0%	04 Apr 26	12Apr-26	04 Apr 26A	12Apr-26A	$000	$000	$0.00	0.00
MLTX02-004EN-566	PreQualifcation SubmittalforMarking Paint	8.00	100%	100%	04 Apr 26	12Apr-26	04 Apr 26A	12Apr-26A	$000	$000	$0.00	0.00
MLTX02-004EN-567	PreQualifcation Appovalfor MakingPaint	5.00	100%	100%	07 Apr 26	12Apr-26	07 Apr 26A	12Apr-26A	$000	$000	$0.00	0.00
PACKAGE ACUNITS		1100	0%	0%	04 Apr 26	15Apr-26	04 Apr 26A	15Apr-26A	$000	$000	$0.00	0.00
MLTX02-004EN-569	PreQualifcation SubmittalforPackageAC Units	9.00	100%	100%	04 Apr 26	13Apr-26	04 Apr 26A	13Apr-26A	$000	$000	$0.00	0.00
MLTX02-004EN-570	PreQualifcation Appovalfor PackageAC Units	3.00	100%	100%	13 Apr 26	15Apr-26	13 Apr 26A	15Apr-26A	$000	$000	$0.00	0.00
AIRDFUSSERS/GRILLS		1100	0%	0%	04 Apr 26	15Apr-26	04 Apr 26A	15Apr-26A	$000	$000	$0.00	0.00
MLTX02-004EN-572	PreQualifcation SubmittalforAir Dfussers/Grills	9.00	100%	100%	04 Apr 26	13Apr-26	04 Apr 26A	13Apr-26A	$000	$000	$0.00	0.00
MLTX02-004EN-573	PreQualifcation Appovalfor Air Dfussers/Grills	3.00	100%	100%	13 Apr 26	15Apr-26	13 Apr 26A	15Apr-26A	$000	$000	$0.00	0.00
GALVANIZEDD UCTS		1100	0%	0%	04 Apr 26	15Apr-26	04 Apr 26A	15Apr-26A	$000	$000	$0.00	0.00
MLTX02-004EN-575	PreQualifcation SubmittalforGalvanized Duct	9.00	100%	100%	04 Apr 26	13Apr-26	04 Apr 26A	13Apr-26A	$000	$000	$0.00	0.00
MLTX02-004EN-576	PreQualifcation Appovalfor Galvanized Duct	3.00	100%	100%	13 Apr 26	15Apr-26	13 Apr 26A	15Apr-26A	$000	$000	$0.00	0.00
EXHAUSTFANS		1100	0%	0%	04 Apr 26	15Apr-26	04 Apr 26A	15Apr-26A	$000	$000	$0.00	0.00
MLTX02-004EN-578	PreQualifcation SubmittalforExhaustFans	9.00	100%	100%	04 Apr 26	13Apr-26	04 Apr 26A	13Apr-26A	$000	$000	$0.00	0.00
MLTX02-004EN-579	PreQualifcation Appovalfor ExhaustFans	3.00	100%	100%	13 Apr 26	15Apr-26	13 Apr 26A	15Apr-26A	$000	$000	$0.00	0.00
DISTRBUTON BOARDS		1100	0%	0%	04 Apr 26	15Apr-26	04 Apr 26A	15Apr-26A	$000	$000	$0.00	0.00
MLTX02-004EN-581	PreQualifcation SubmittalforDistribution Boards	9.00	100%	100%	04 Apr 26	13Apr-26	04 Apr 26A	13Apr-26A	$000	$000	$0.00	0.00
MLTX02-004EN-582	PreQualifcation Appovalfor Distribution Boards	3.00	100%	100%	13 Apr 26	15Apr-26	13 Apr 26A	15Apr-26A	$000	$000	$0.00	0.00
POWERCABLES		1100	0%	0%	04 Apr 26	15Apr-26	04 Apr 26A	15Apr-26A	$000	$000	$0.00	0.00
MLTX02-004EN-584	PreQualifcation SubmittalforPowerCables	9.00	100%	100%	04 Apr 26	13Apr-26	04 Apr 26A	13Apr-26A	$000	$000	$0.00	0.00
MLTX02-004EN-585	PreQualifcation Appovalfor Power Calles	3.00	100%	100%	13 Apr 26	15Apr-26	13 Apr 26A	15Apr-26A	$000	$000	$0.00	0.00
LIGHTFIXTURES		1100	0%	0%	04 Apr 26	15Apr-26	04 Apr 26A	15Apr-26A	$000	$000	$0.00	0.00
MLTX02-004EN-587	PreQualifcation SubmittalforLightFixtures	9.00	100%	100%	04 Apr 26	13Apr-26	04 Apr 26A	13Apr-26A	$000	$000	$0.00	0.00
MLTX02-004EN-588	PreQualifcation Appovalfor lightFixtures	3.00	100%	100%	13 Apr 26	15Apr-26	13 Apr 26A	15Apr-26A	$000	$000	$0.00	0.00
CCTV MATERALS		8.00	0%	0%	04 Apr 26	12Apr-26	04 Apr 26A	12Apr-26A	$000	$000	$0.00	0.00
MLTX02-004EN-590	PreQualifcation SubmittalforCCTV	3.00	100%	100%	04 Apr 26	06Apr-26	04 Apr 26A	06Apr-26A	$000	$000	$0.00	0.00
MLTX02-004EN-591	PreQualifcation Appovalfor CCTV	5.00	100%	100%	07 Apr 26	12Apr-26	07 Apr 26A	12Apr-26A	$000	$000	$0.00	0.00
POWEROUTIETS/SWITCHES		1100	0%	0%	04 Apr 26	15Apr-26	04 Apr 26A	15Apr-26A	$000	$000	$0.00	0.00
MLTX02-004EN-593	PreQualifcation SubmittalforPowerOutlets/Switches	9.00	100%	100%	04 Apr 26	13Apr-26	04 Apr 26A	13Apr-26A	$000	$000	$0.00	0.00
MLTX02-004EN-594	PreQualifcation Appovalfor Power OutetsSwitches	3.00	100%	100%	13 Apr 26	15Apr-26	13 Apr 26A	15Apr-26A	$000	$000	$0.00	0.00
LANDSCAPE WORKS		4200	0%	0%	04 Apr 26	21May-26	04 Apr 26A	21May-26A	$000	$000	$0.00	0.00
INTERLOCKNG PAVING		1800	0%	0%	04 Apr 26	23Apr-26	04 Apr 26A	23Apr-26A	$000	$000	$0.00	0.00
MLTX02-004EN-597	PreQualifcation SubmittalforInterlocking Block Paves	8.00	100%	100%	04 Apr 26	12Apr-26	04 Apr 26A	12Apr-26A	$000	$000	$0.00	0.00
MLTX02-004EN-598	PreQualifcation Appovalfor Interbcking BlockPavers	1100	100%	100%	12 Apr 26	23Apr-26	12 Apr 26A	23Apr-26A	$000	$000	$0.00	0.00
CURBSTONE		1800	0%	0%	04 Apr 26	23Apr-26	04 Apr 26A	23Apr-26A	$000	$000	$0.00	0.00
MLTX02-004EN-600	PreQualifcation SubmittalforCurbstne	8.00	100%	100%	04 Apr 26	12Apr-26	04 Apr 26A	12Apr-26A	$000	$000	$0.00	0.00
MLTX02-004EN-601	PreQualifcation Appovalfor Cubstone	1100	100%	100%	12 Apr 26	23Apr-26	12 Apr 26A	23Apr-26A	$000	$000	$0.00	0.00

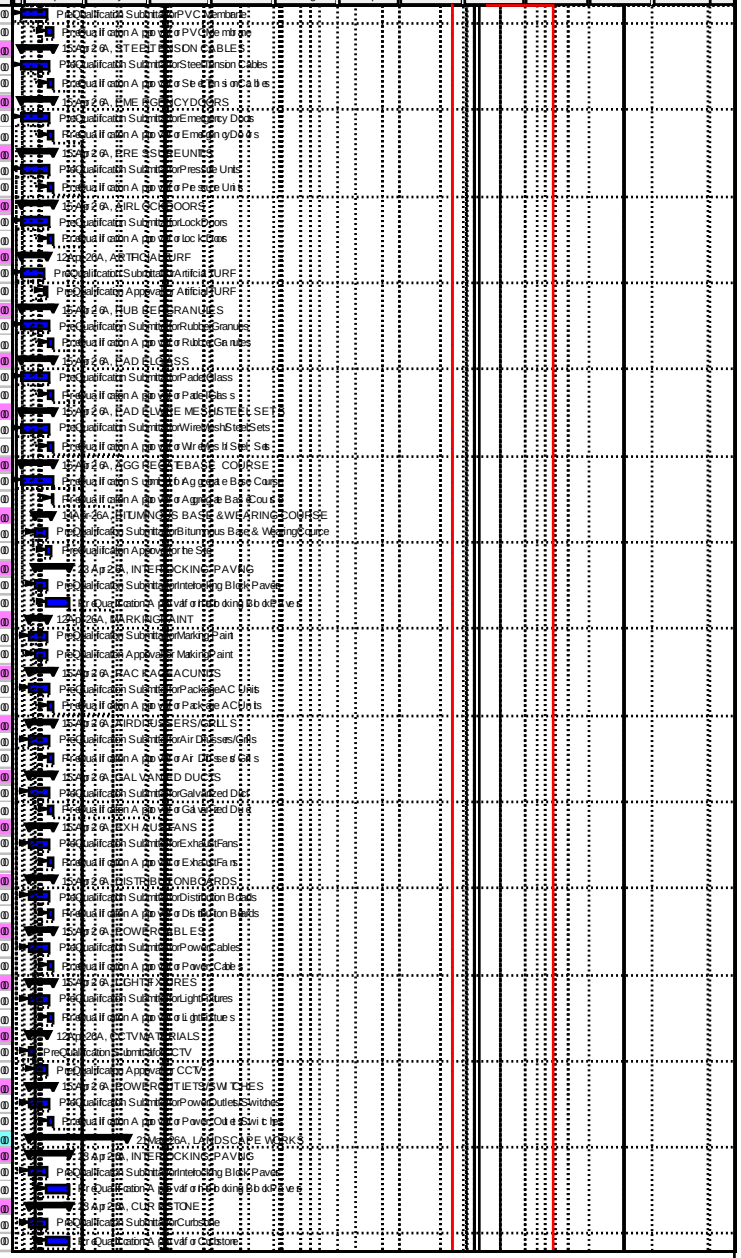

© Oracle Corporation

ActivityID	ActivityName	Orginal Duration	Schedule %	Performance% Complete	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Variance - BL Project
	PAVEMENT MARKING	8.00	0%	0%	04-Apr-26	12-Apr-26	01-Apr-26 A	12-Apr-26 A	$000	$000	$0.00	0.00
MLTX-02-004EN-603	PreQualification Submittal for Pavement Markings	3.00	100%	100%	04-Apr-26	06-Apr-26	01-Apr-26 A	06-Apr-26 A	$000	$000	$0.00	0.00
MLTX-02-004EN-604	PreQualification Approval for Pavement Markings	5.00	100%	100%	07-Apr-26	12-Apr-26	07-Apr-26 A	12-Apr-26 A	$000	$000	$0.00	0.00
	TRAFFIC SIGNS	1400	0%	0%	06-May-26	21-May-26	06-May-26 A	21-May-26 A	$000	$000	$0.00	0.00
MLTX-02-004EN-606	PreQualification Submittal for Traffic Signs	1.00	100%	100%	06-May-26	06-May-26	06-May-26 A	06-May-26 A	$000	$000	$0.00	0.00
MLTX-02-004EN-607	PreQualification Approval for Traffic Signs	1.00	100%	100%	21-May-26	21-May-26	21-May-26 A	21-May-26 A	$000	$000	$0.00	0.00
	IRRGATION PIPES PRINKLERS	4200	0%	0%	04-Apr-26	21-May-26	01-Apr-26 A	21-May-26 A	$000	$000	$0.00	0.00
MLTX-02-004EN-609	PreQualification Submittal for Irrigation Pipes/Sprinkles	2000	100%	100%	04-Apr-26	26-Apr-26	01-Apr-26 A	26-Apr-26 A	$000	$000	$0.00	0.00
MLTX-02-004EN-610	PreQualification Approval for Irrigation Pipes Sprinkles	1.00	100%	100%	21-May-26	21-May-26	21-May-26 A	21-May-26 A	$000	$000	$0.00	0.00
	AGRICULTURE SOIL	4200	0%	0%	04-Apr-26	21-May-26	01-Apr-26 A	21-May-26 A	$000	$000	$0.00	0.00
MLTX-02-004EN-612	PreQualification Submittal for Agriculture Soil	2000	100%	100%	04-Apr-26	26-Apr-26	01-Apr-26 A	26-Apr-26 A	$000	$000	$0.00	0.00
MLTX-02-004EN-613	PreQualification Approval for Agricuture Soil	1.00	100%	100%	21-May-26	21-May-26	21-May-26 A	21-May-26 A	$000	$000	$0.00	0.00
	TRACK SURFACE	8.00	0%	0%	04-Apr-26	12-Apr-26	01-Apr-26 A	12-Apr-26 A	$000	$000	$0.00	0.00
MLTX-02-004EN-615	PreQualification Submittal for Track Surface	3.00	100%	100%	04-Apr-26	06-Apr-26	01-Apr-26 A	06-Apr-26 A	$000	$000	$0.00	0.00
MLTX-02-004EN-616	PreQualification Approval for Track Surface	5.00	100%	100%	07-Apr-26	12-Apr-26	07-Apr-26 A	12-Apr-26 A	$000	$000	$0.00	0.00
	GRASS/TREES	1400	0%	0%	04-Apr-26	19-Apr-26	01-Apr-26 A	19-Apr-26 A	$000	$000	$0.00	0.00
MLTX-02-004EN-618	PreQualification Submittal for Grass/Trees	1000	100%	100%	04-Apr-26	14-Apr-26	01-Apr-26 A	14-Apr-26 A	$000	$000	$0.00	0.00
MLTX-02-004EN-619	PreQualification Approval for Gass/Tees	5.00	100%	100%	14-Apr-26	19-Apr-26	14-Apr-26 A	19-Apr-26 A	$000	$000	$0.00	0.00
	CABIES	2.00	0%	0%	06-May-26	07-May-26	06-May-26 A	07-May-26 A	$000	$000	$0.00	0.00
MLTX-02-004EN-621	PreQualification Submittal for Cables	1.00	100%	100%	06-May-26	06-May-26	06-May-26 A	06-May-26 A	$000	$000	$0.00	0.00
MLTX-02-004EN-622	PreQualification Approval for Cables	1.00	100%	100%	07-May-26	07-May-26	07-May-26 A	07-May-26 A	$000	$000	$0.00	0.00
	LIGHT POLES	2.00	0%	0%	06-May-26	07-May-26	06-May-26 A	07-May-26 A	$000	$000	$0.00	0.00
MLTX-02-004EN-624	PreQualification Submittal for Lighting poles	1.00	100%	100%	06-May-26	06-May-26	06-May-26 A	06-May-26 A	$000	$000	$0.00	0.00
MLTX-02-004EN-625	PreQualification Approval for Lighting poles	1.00	100%	100%	07-May-26	07-May-26	07-May-26 A	07-May-26 A	$000	$000	$0.00	0.00
	MATERIALS UBMITTAL & APPROVAL	20300	0%	0%	11-Apr-26	02-Sep-26	11-Apr-26 A	07-Dec-26	$000	$000	$0.00	-8100
	TOILET/SERVICE WORKS	9200	0%	0%	11-Apr-26	12-Jul-26	11-Apr-26 A	22-Jul-26 A	$000	$000	$0.00	-900
	STEEL REINFORCEMENT	4.00	0%	0%	11-Apr-26	14-Apr-26	11-Apr-26 A	14-Apr-26 A	$000	$000	$0.00	0.00
MLTX-02-004EN-625	Material Submittal for Steel Reinforcement	2.00	100%	100%	11-Apr-26	12-Apr-26	11-Apr-26 A	12-Apr-26 A	$000	$000	$0.00	0.00
MLTX-02-004EN-630	Material Approval for Steel Reinforcement	3.00	100%	100%	12-Apr-26	14-Apr-26	12-Apr-26 A	14-Apr-26 A	$000	$000	$0.00	0.00
	READY MIX CONCRETE	1000	0%	0%	15-Apr-26	26-Apr-26	15-Apr-26 A	26-Apr-26 A	$000	$000	$0.00	0.00
MLTX-02-004EN-632	Material Submittal for Ready Mixed Concrete	3.00	100%	100%	15-Apr-26	18-Apr-26	15-Apr-26 A	18-Apr-26 A	$000	$000	$0.00	0.00
MLTX-02-004EN-633	Material Approval of Ready Mixed Concrete	7.00	100%	100%	19-Apr-26	26-Apr-26	19-Apr-26 A	26-Apr-26 A	$000	$000	$0.00	0.00
	CONCRETE BLOCKS	1000	0%	0%	15-Apr-26	26-Apr-26	15-Apr-26 A	26-Apr-26 A	$000	$000	$0.00	0.00
MLTX-02-004EN-635	Material Submittal for Concrete Blocks	3.00	100%	100%	15-Apr-26	18-Apr-26	15-Apr-26 A	18-Apr-26 A	$000	$000	$0.00	0.00
MLTX-02-004EN-636	Material Approval for Concete Blocks	7.00	100%	100%	19-Apr-26	26-Apr-26	19-Apr-26 A	26-Apr-26 A	$000	$000	$0.00	0.00
	FLOOR/WALL TILES	8800	0%	0%	15-Apr-26	12-Jul-26	15-Apr-26 A	22-Jul-26 A	$000	$000	$0.00	-900
MLTX-02-004EN-641	Material Submittal for Tiling Materials	3.00	100%	100%	15-Apr-26	18-Apr-26	15-Apr-26 A	18-Apr-26 A	$000	$000	$0.00	0.00
MLTX-02-004EN-642	Material Approval for Tiling Material	7.00	100%	100%	05-Jul-26	12-Jul-26	22-Jul-26 A	22-Jul-26 A	$000	$000	$0.00	6.00
	SUSPENDED CEILING	5.00	0%	0%	15-Apr-26	20-Apr-26	15-Apr-26 A	20-Apr-26 A	$000	$000	$0.00	0.00
MLTX-02-004EN-644	Material Submittal for Suspend Ceiling	3.00	100%	100%	15-Apr-26	18-Apr-26	15-Apr-26 A	18-Apr-26 A	$000	$000	$0.00	0.00
MLTX-02-004EN-645	Material Approval for Suspend Ceiling	2.00	100%	100%	19-Apr-26	20-Apr-26	19-Apr-26 A	20-Apr-26 A	$000	$000	$0.00	0.00
	DOORS/WINDOWS	1400	0%	0%	06-May-26	21-May-26	06-May-26 A	21-May-26 A	$000	$000	$0.00	0.00
MLTX-02-004EN-647	Material Submittal for Doos/Windows	1.00	100%	100%	06-May-26	06-May-26	06-May-26 A	06-May-26 A	$000	$000	$0.00	0.00
MLTX-02-004EN-648	Material Approval for Doors/Windows	1.00	100%	100%	21-May-26	21-May-26	21-May-26 A	21-May-26 A	$000	$000	$0.00	0.00
	FURNITURES	2.00	0%	0%	06-May-26	07-May-26	06-May-26 A	07-May-26 A	$000	$000	$0.00	0.00
MLTX-02-004EN-650	Material Submittal for Furnitures	1.00	100%	100%	06-May-26	06-May-26	06-May-26 A	06-May-26 A	$000	$000	$0.00	0.00
MLTX-02-004EN-651	Material Approval for Furnitures	1.00	100%	100%	07-May-26	07-May-26	07-May-26 A	07-May-26 A	$000	$000	$0.00	0.00
	SANITARY FIXTURES	1400	0%	0%	15-Apr-26	30-Apr-26	15-Apr-26 A	30-Apr-26 A	$000	$000	$0.00	0.00
MLTX-02-004EN-653	Material Submittal for Sanitary Fixtures	6.00	100%	100%	15-Apr-26	21-Apr-26	15-Apr-26 A	21-Apr-26 A	$000	$000	$0.00	0.00
MLTX-02-004EN-654	Material Approval for Sanitary fixtures	1100	100%	100%	19-Apr-26	30-Apr-26	19-Apr-26 A	30-Apr-26 A	$000	$000	$0.00	0.00
	WATER SUPPLY PIPES	2.00	0%	0%	15-Apr-26	16-Apr-26	15-Apr-26 A	16-Apr-26 A	$000	$000	$0.00	0.00
MLTX-02-004EN-656	Material Submittal for Water Supply Pipes	1.00	100%	100%	15-Apr-26	15-Apr-26	15-Apr-26 A	15-Apr-26 A	$000	$000	$0.00	0.00
MLTX-02-004EN-657	Material Approval for Water Supply Pipes	2.00	100%	100%	15-Apr-26	16-Apr-26	15-Apr-26 A	16-Apr-26 A	$000	$000	$0.00	0.00
	SEWAGE DRAINAGE PIPES	2.00	0%	0%	15-Apr-26	16-Apr-26	15-Apr-26 A	16-Apr-26 A	$000	$000	$0.00	0.00
MLTX-02-004EN-659	Material Submittal for Sewage/Drainage Pipes	1.00	100%	100%	15-Apr-26	15-Apr-26	15-Apr-26 A	15-Apr-26 A	$000	$000	$0.00	0.00
MLTX-02-004EN-660	Material Approval for Sewage Drainage Pipes	2.00	100%	100%	15-Apr-26	16-Apr-26	15-Apr-26 A	16-Apr-26 A	$000	$000	$0.00	0.00
	PACKAGE ACUNITS	2.00	0%	0%	06-May-26	07-May-26	06-May-26 A	07-May-26 A	$000	$000	$0.00	0.00
MLTX-02-004EN-662	Material Submittal for Package AC Units	1.00	100%	100%	06-May-26	06-May-26	06-May-26 A	06-May-26 A	$000	$000	$0.00	0.00
MLTX-02-004EN-663	Material Approval for Package AC Units	1.00	100%	100%	07-May-26	07-May-26	07-May-26 A	07-May-26 A	$000	$000	$0.00	0.00
	AIR DIFFUSSERS/GRILLS	1800	0%	0%	16-Apr-26	06-May-26	16-Apr-26 A	06-May-26 A	$000	$000	$0.00	0.00
MLTX-02-004EN-665	Material Submittal for Air Diffusers/Grills	6.00	100%	100%	16-Apr-26	22-Apr-26	16-Apr-26 A	22-Apr-26 A	$000	$000	$0.00	0.00
MLTX-02-004EN-666	Material Approval for Air Diffusers/Grills	1.00	100%	100%	06-May-26	06-May-26	06-May-26 A	06-May-26 A	$000	$000	$0.00	0.00
	GALVANIZED DUCTS	6.00	0%	0%	13-Jun-26	18-Jun-26	13-Jun-26 A	18-Jun-26 A	$000	$000	$0.00	0.00
MLTX-02-004EN-668	Material Submittal for Galvanized Ducts	1.00	100%	100%	13-Jun-26	13-Jun-26	13-Jun-26 A	13-Jun-26 A	$000	$000	$0.00	0.00
MLTX-02-004EN-669	Material Approval for Galvanized Ducts	1.00	100%	100%	18-Jun-26	18-Jun-26	18-Jun-26 A	18-Jun-26 A	$000	$000	$0.00	0.00
	EXHAUST FANS	1800	0%	0%	16-Apr-26	06-May-26	16-Apr-26 A	06-May-26 A	$000	$000	$0.00	0.00
MLTX-02-004EN-671	Material Submittal for Exhaust Fans	2.00	100%	100%	16-Apr-26	18-Apr-26	16-Apr-26 A	18-Apr-26 A	$000	$000	$0.00	0.00
MLTX-02-004EN-672	Material Approval for Exhaust Fans	1.00	100%	100%	06-May-26	06-May-26	06-May-26 A	06-May-26 A	$000	$000	$0.00	0.00
	LIGHTING FIXTURES	8.00	0%	0%	16-Apr-26	25-Apr-26	16-Apr-26 A	25-Apr-26 A	$000	$000	$0.00	0.00
MLTX-02-004EN-674	Material Submittal for Lighting Fixtures	3.00	100%	100%	16-Apr-26	19-Apr-26	16-Apr-26 A	19-Apr-26 A	$000	$000	$0.00	0.00
MLTX-02-004EN-675	Material Approval for Lighting Fixtures	5.00	100%	100%	20-Apr-26	25-Apr-26	20-Apr-26 A	25-Apr-26 A	$000	$000	$0.00	0.00
	SWITCHES/SOCKETS	8.00	0%	0%	16-Apr-26	25-Apr-26	16-Apr-26 A	25-Apr-26 A	$000	$000	$0.00	0.00
MLTX-02-004EN-677	Material Submittal for Switches/Sockets	3.00	100%	100%	16-Apr-26	19-Apr-26	16-Apr-26 A	19-Apr-26 A	$000	$000	$0.00	0.00

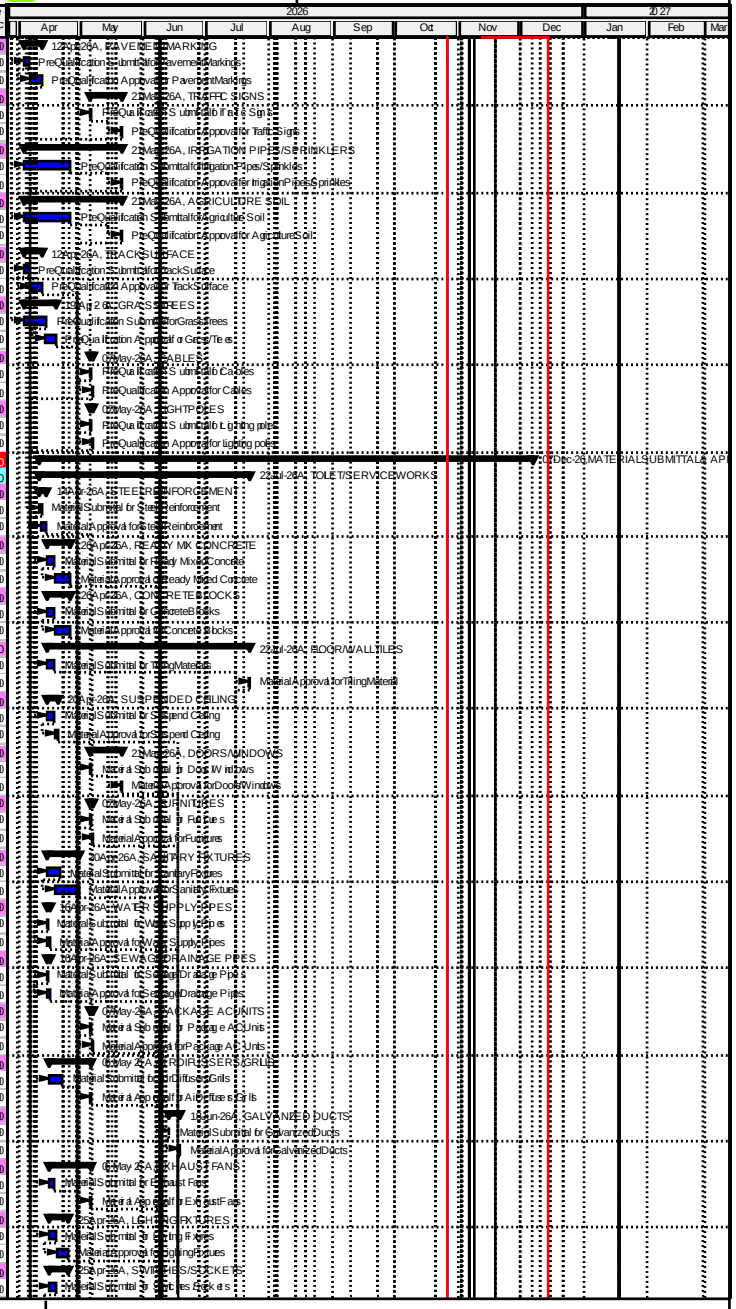


Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work

TASK filter: All Activities


© Oracle Corporation

ActivityID	ActivityName	Orginal Duration	Schedule %	Performance% Complete	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Variance - BL Project
MLTX02-004EN-678	Material Approval for Switches/Sockets	5.00	100%	100%	20-Apr-26	25-Apr-26	20-Apr-26 A	25-Apr-26 A	$000	$000	$0.00	0.00
EARTHINGSYSTEM		2.00	0%	0%	06-May-26	07-May-26	06-May-26 A	07-May-26 A	$000	$000	$0.00	0.00
MLTX02-004EN-680	Material Submittal for EarthingSystem	1.00	100%	100%	06-May-26	06-May-26	06-May-26 A	06-May-26 A	$000	$000	$0.00	0.00
MLTX02-004EN-681	Material Approval for Earthing System	1.00	100%	100%	07-May-26	07-May-26	07-May-26 A	07-May-26 A	$000	$000	$0.00	0.00
DISTRIBUTION PANNELS		8.00	0%	0%	16-Apr-26	25-Apr-26	16-Apr-26 A	25-Apr-26 A	$000	$000	$0.00	0.00
MLTX02-004EN-682	Material Submittal for Distribution Panels	3.00	100%	100%	16-Apr-26	19-Apr-26	16-Apr-26 A	19-Apr-26 A	$000	$000	$0.00	0.00
MLTX02-004EN-684	Material Approval for Distibuton Panels	5.00	100%	100%	20-Apr-26	25-Apr-26	20-Apr-26 A	25-Apr-26 A	$000	$000	$0.00	0.00
PLAYGROUND WORKS		20200	0%	0%	12-Apr-26	02-Sep-26	12-Apr-26 A	07-Dec-26	$000	$000	$0.00	-8100
PVC MEMBRANE		17100	0%	0%	15-Apr-26	13-Jul-26	15-Apr-26 A	04-Nov-26	$000	$000	$0.00	-9700
MLTX02-004EN-688	Material Approval for PVC Membane	8.00	100%	0%	05-Jul-25	13-Jul-26	27-Oct-26	04-Nov-26	$000	$000	$0.00	0.00
MLTX02-004EN-687	Material Submittal for PVC Membrane	3.00	100%	100%	15-Apr-26	18-Apr-26	15-Apr-26 A	18-Apr-26 A	$000	$000	$0.00	0.00
STEEL TENSION CABLES		16200	0%	0%	06-May-26	23-Jul-26	06-May-26 A	15-Nov-26	$000	$000	$0.00	-9700
MLTX02-004EN-691	Material Approval for Steel Tension Cables	9.00	100%	0%	14-Jul-25	23-Jul-26	05-Nov-26	15-Nov-26	$000	$000	$0.00	0.00
MLTX02-004EN-690	Material Submittal for Steel TensionCables	1.00	100%	100%	06-May-26	06-May-26	06-May-26 A	06-May-26 A	$000	$000	$0.00	0.00
EMERGENCY DOORS		17100	0%	0%	06-May-26	03-Aug-26	06-May-26 A	25-Nov-26	$000	$000	$0.00	-9700
MLTX02-004EN-694	Material Approval for Emergency Doors	9.00	100%	0%	25-Jul-25	03-Aug-26	16-Nov-26	25-Nov-26	$000	$000	$0.00	0.00
MLTX02-004EN-693	Material Submittal for Emegency Doors	1.00	100%	100%	06-May-26	06-May-26	06-May-26 A	06-May-26 A	$000	$000	$0.00	0.00
PRESSURE UNITS		17100	0%	0%	06-May-26	13-Aug-26	06-May-26 A	24-Aug-26 A	$000	$000	$0.00	-900
MLTX02-004EN-696	Material Submittal for PressureUnits	1.00	100%	100%	06-May-26	06-May-26	06-May-26 A	06-May-26 A	$000	$000	$0.00	0.00
MLTX02-004EN-697	Material Approval for Pressure Units	9.00	100%	100%	04-Aug-26	13-Aug-26	21-Aug-26 A	24-Aug-26 A	$000	$000	$0.00	8.00
AIRLOCK DOORS		17300	0%	0%	06-May-26	24-Aug-26	06-May-26 A	28-Nov-26	$000	$000	$0.00	-8100
MLTX02-004EN-700	Material Approval for Lock Doors	8.00	100%	0%	16-Aug-26	24-Aug-26	19-Nov-26	28-Nov-26	$000	$000	$0.00	0.00
MLTX02-004EN-699	Material Submittal for Lock Doors	1.00	100%	100%	06-May-26	06-May-26	06-May-26 A	06-May-26 A	$000	$000	$0.00	0.00
ARTIFICIAL TURF		1700	0%	0%	12-Apr-26	30-Apr-26	12-Apr-26 A	30-Apr-26 A	$000	$000	$0.00	0.00
MLTX02-004EN-702	Material Submittal for Artificial TURF	1500	100%	100%	12-Apr-26	28-Apr-26	12-Apr-26 A	28-Apr-26 A	$000	$000	$0.00	0.00
MLTX02-004EN-703	Material Approval for Artificial TURF	3.00	100%	100%	28-Apr-26	30-Apr-26	28-Apr-26 A	30-Apr-26 A	$000	$000	$0.00	0.00
RUBBER GRANULES		1400	0%	0%	06-May-26	21-May-26	06-May-26 A	21-May-26 A	$000	$000	$0.00	0.00
MLTX02-004EN-705	Material Submittal for Rubber Granules	1.00	100%	100%	06-May-26	06-May-26	06-May-26 A	06-May-26 A	$000	$000	$0.00	0.00
MLTX02-004EN-706	Material Approval for RubberGranules	1.00	100%	100%	21-May-26	21-May-26	21-May-26 A	21-May-26 A	$000	$000	$0.00	0.00
PADEL GLASS		1400	0%	0%	06-May-26	21-May-26	06-May-26 A	21-May-26 A	$000	$000	$0.00	0.00
MLTX02-004EN-708	Material Submittal for Padel Glass	1.00	100%	100%	06-May-26	06-May-26	06-May-26 A	06-May-26 A	$000	$000	$0.00	0.00
MLTX02-004EN-709	Material Approval for PadelGlass	1.00	100%	100%	21-May-26	21-May-26	21-May-26 A	21-May-26 A	$000	$000	$0.00	0.00
PADEL WIRE MESH/STEEL SETS		16500	0%	0%	25-May-26	02-Sep-26	25-May-26 A	07-Dec-26	$000	$000	$0.00	-8100
MLTX02-004EN-712	Material Approval for Wie MeshSteel Sets	8.00	100%	0%	25-Aug-26	02-Sep-26	29-Nov-26	07-Dec-26	$000	$000	$0.00	0.00
MLTX02-004EN-711	Material Submittal for Wire Mesh/Steel Sets	1.00	100%	100%	25-May-26	25-May-26	25-May-26 A	25-May-26 A	$000	$000	$0.00	0.00
AGGREGATE BASE COURSE		2200	0%	0%	21-May-26	18-Jun-26	21-May-26 A	18-Jun-26 A	$000	$000	$0.00	0.00
MLTX02-004EN-714	Material Submittal for AggegateBase Course	1.00	100%	100%	21-May-26	21-May-26	21-May-26 A	21-May-26 A	$000	$000	$0.00	0.00
MLTX02-004EN-715	Material Approval for Aggregate Base Couse	1.00	100%	100%	18-Jun-26	18-Jun-26	18-Jun-26 A	18-Jun-26 A	$000	$000	$0.00	0.00
BITUMINOUS BASE & WEARING COURSE		2.00	0%	0%	16-Apr-26	18-Apr-26	16-Apr-26 A	18-Apr-26 A	$000	$000	$0.00	0.00
MLTX02-004EN-717	Material Submittal for BituminousBase& Wearing Couce	2.00	100%	100%	16-Apr-26	18-Apr-26	16-Apr-26 A	18-Apr-26 A	$000	$000	$0.00	0.00
MLTX02-004EN-718	Material Approval for theSite	1.00	100%	100%	18-Apr-26	18-Apr-26	18-Apr-26 A	18-Apr-26 A	$000	$000	$0.00	0.00
INTERLOCKING PAVING		1.00	0%	0%	21-May-26	21-May-26	21-May-26 A	21-May-26 A	$000	$000	$0.00	0.00
MLTX02-004EN-720	Material Submittal for InterlockingBlockPavers	1.00	100%	100%	21-May-26	21-May-26	21-May-26 A	21-May-26 A	$000	$000	$0.00	0.00
MLTX02-004EN-721	Material Approval for Interlocking Bbck Pavers	1.00	100%	100%	21-May-26	21-May-26	21-May-26 A	21-May-26 A	$000	$000	$0.00	0.00
MARKING PAINT		6.00	0%	0%	13-Apr-26	19-Apr-26	13-Apr-26 A	19-Apr-26 A	$000	$000	$0.00	0.00
MLTX02-004EN-722	Material Submittal for Making Paint	5.00	100%	100%	13-Apr-26	18-Apr-26	13-Apr-26 A	18-Apr-26 A	$000	$000	$0.00	0.00
MLTX02-004EN-724	Material Approval for Marking Paint	2.00	100%	100%	18-Apr-26	19-Apr-26	18-Apr-26 A	19-Apr-26 A	$000	$000	$0.00	0.00
PACKAGE ACUNITS		1.00	0%	0%	21-May-26	21-May-26	21-May-26 A	21-May-26 A	$000	$000	$0.00	0.00
MLTX02-004EN-726	Material Submittal for Package ACUnits	1.00	100%	100%	21-May-26	21-May-26	21-May-26 A	21-May-26 A	$000	$000	$0.00	0.00
MLTX02-004EN-727	Material Approval for Package AC Units	1.00	100%	100%	21-May-26	21-May-26	21-May-26 A	21-May-26 A	$000	$000	$0.00	0.00
AIRDFUSSERS/GRILLS		2100	0%	0%	13-Apr-26	06-May-26	13-Apr-26 A	06-May-26 A	$000	$000	$0.00	0.00
MLTX02-004EN-729	Material Submittal for AirDifussersGrills	9.00	100%	100%	13-Apr-26	22-Apr-26	13-Apr-26 A	22-Apr-26 A	$000	$000	$0.00	0.00
MLTX02-004EN-730	Material Approval for AirDifussers/Grills	1.00	100%	100%	06-May-26	06-May-26	06-May-26 A	06-May-26 A	$000	$000	$0.00	0.00
GALVANIZEDDUCTS		6.00	0%	0%	13-Jun-26	18-Jun-26	13-Jun-26 A	18-Jun-26 A	$000	$000	$0.00	0.00
MLTX02-004EN-732	Material Submittal for GalvanizedDuct	1.00	100%	100%	13-Jun-26	13-Jun-26	13-Jun-26 A	13-Jun-26 A	$000	$000	$0.00	0.00
MLTX02-004EN-733	Material Approval for GalvanizedDuct	1.00	100%	100%	18-Jun-26	18-Jun-26	18-Jun-26 A	18-Jun-26 A	$000	$000	$0.00	0.00
EXHAUST FANS		2100	0%	0%	13-Apr-26	06-May-26	13-Apr-26 A	06-May-26 A	$000	$000	$0.00	0.00
MLTX02-004EN-735	Material Submittal for Exhaust Fans	5.00	100%	100%	13-Apr-26	18-Apr-26	13-Apr-26 A	18-Apr-26 A	$000	$000	$0.00	0.00
MLTX02-004EN-736	Material Approval for Exhaust Fans	1.00	100%	100%	06-May-26	06-May-26	06-May-26 A	06-May-26 A	$000	$000	$0.00	0.00
DISTRIBUTION BOARDS		1100	0%	0%	13-Apr-26	25-Apr-26	13-Apr-26 A	25-Apr-26 A	$000	$000	$0.00	0.00
MLTX02-004EN-738	Material Submittal for DistributionBoards	6.00	100%	100%	13-Apr-26	19-Apr-26	13-Apr-26 A	19-Apr-26 A	$000	$000	$0.00	0.00
MLTX02-004EN-739	Material Approval for Distibuton Boards	6.00	100%	100%	19-Apr-26	25-Apr-26	19-Apr-26 A	25-Apr-26 A	$000	$000	$0.00	0.00
POWER CABLES		7.00	0%	0%	13-Apr-26	20-Apr-26	13-Apr-26 A	20-Apr-26 A	$000	$000	$0.00	0.00
MLTX02-004EN-741	Material Submittal for PowerCables	5.00	100%	100%	13-Apr-26	18-Apr-26	13-Apr-26 A	18-Apr-26 A	$000	$000	$0.00	0.00
MLTX02-004EN-742	Material Approval for PowerCables	4.00	100%	100%	16-Apr-26	20-Apr-26	16-Apr-26 A	20-Apr-26 A	$000	$000	$0.00	0.00
LIGHT FIXTURES		9.00	0%	0%	13-Apr-26	22-Apr-26	13-Apr-26 A	22-Apr-26 A	$000	$000	$0.00	0.00
MLTX02-004EN-744	Material Submittal for Light Fixtures	3.00	100%	100%	13-Apr-26	15-Apr-26	13-Apr-26 A	15-Apr-26 A	$000	$000	$0.00	0.00
MLTX02-004EN-745	Material Approval for Light Fixtures	6.00	100%	100%	16-Apr-26	22-Apr-26	16-Apr-26 A	22-Apr-26 A	$000	$000	$0.00	0.00
CCTV MATERIALS		9.00	0%	0%	13-Apr-26	22-Apr-26	13-Apr-26 A	22-Apr-26 A	$000	$000	$0.00	0.00
MLTX02-004EN-747	Material Submittal for CCTV	3.00	100%	100%	13-Apr-26	15-Apr-26	13-Apr-26 A	15-Apr-26 A	$000	$000	$0.00	0.00
MLTX02-004EN-748	Material Approval for CCTV	6.00	100%	100%	16-Apr-26	22-Apr-26	16-Apr-26 A	22-Apr-26 A	$000	$000	$0.00	0.00
POWER OUTLETS/SWITCHES		2.00	0%	0%	06-May-26	07-May-26	06-May-26 A	07-May-26 A	$000	$000	$0.00	0.00

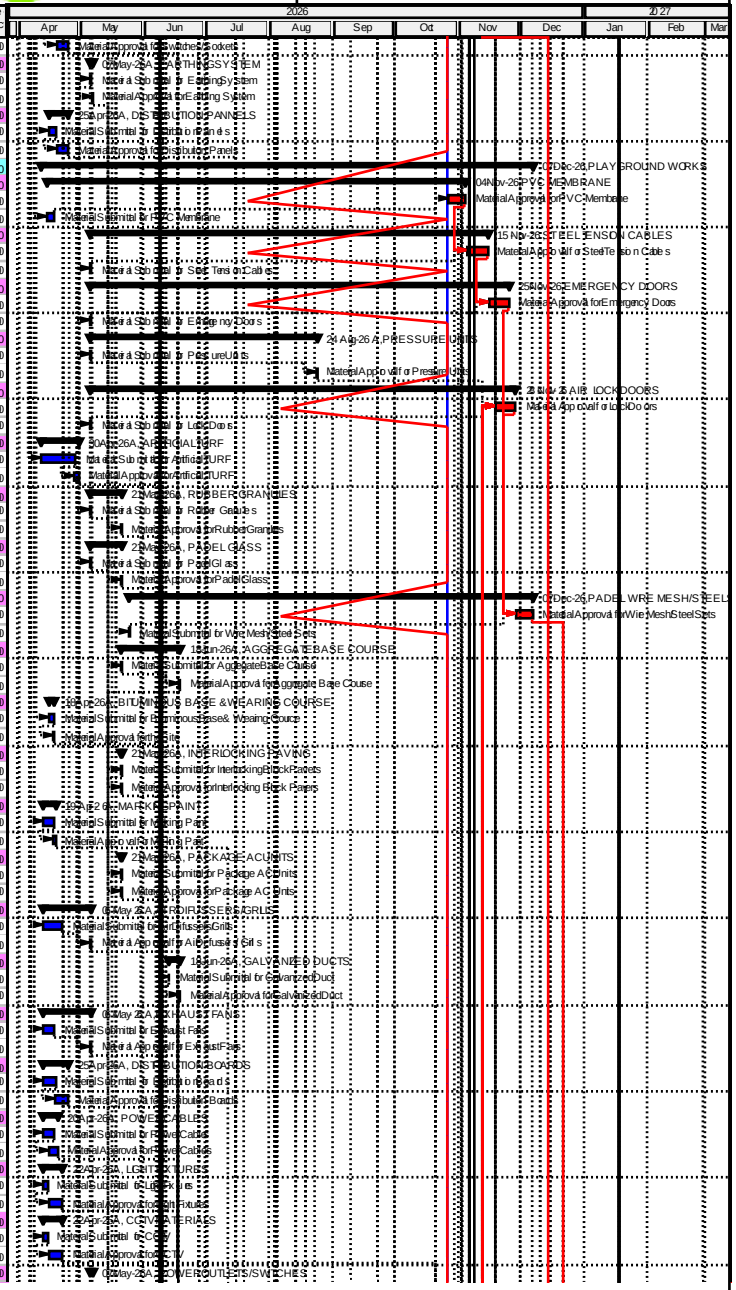

© Oracle Corporation

ActivityID	ActivityName	Orginal Duration	Schedule %	Performance% Complete	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Variance - BL Project
MLTX02-004EN-750	Material Submittal for PowerOutlets/Switches	1.00	100%	100%	06-May-26	06May-26	06 May 26 A	06May-26A	$000	$000	$0.00	0.00
MLTX02-004EN-751	Material Approval forPowerOutlets/Switches	1.00	100%	100%	07-May-26	07May-26	07 May 26 A	07May-26A	$000	$000	$0.00	0.00
LANDSCAPE WORKS		9300	0%	0%	13 Apr 26	11Jul-26	13 Apr 26 A	27Jul-26A	$000	$000	$0.00	-1400
INTERLOCKNG PAVING		9.00	0%	0%	13 Apr 26	22Apr-26	13 Apr 26 A	22Apr-26A	$000	$000	$0.00	0.00
MLTX02-004EN-754	Material Submittal for InterlockingBlockPavers	3.00	100%	100%	13 Apr 26	15Apr-26	13 Apr 26 A	15Apr-26A	$000	$000	$0.00	0.00
MLTX02-004EN-755	Material Approval forInterlocking Block Pavers	6.00	100%	100%	16 Apr 26	22Apr-26	16 Apr 26 A	22Apr-26A	$000	$000	$0.00	0.00
CURBSTONE		9.00	0%	0%	13 Apr 26	22Apr-26	13 Apr 26 A	22Apr-26A	$000	$000	$0.00	0.00
MLTX02-004EN-757	Material Submittal for Cubstone	3.00	100%	100%	13 Apr 26	15Apr-26	13 Apr 26 A	15Apr-26A	$000	$000	$0.00	0.00
MLTX02-004EN-758	Material Approval forCurbstone	6.00	100%	100%	16 Apr 26	22Apr-26	16 Apr 26 A	22Apr-26A	$000	$000	$0.00	0.00
PAVEMENT MARKNG		6.00	0%	0%	13 Apr 26	19Apr-26	13 Apr 26 A	19Apr-26A	$000	$000	$0.00	0.00
MLTX02-004EN-760	Material Submittal for Pavement Makings	5.00	100%	100%	13 Apr 26	18Apr-26	13 Apr 26 A	18Apr-26A	$000	$000	$0.00	0.00
MLTX02-004EN-761	Material Approval forPavement Makings	2.00	100%	100%	18 Apr 26	19Apr-26	18 Apr 26 A	19Apr-26A	$000	$000	$0.00	0.00
TRAFFC SGNS		9.00	0%	0%	13 Apr 26	22Apr-26	13 Apr 26 A	22Apr-26A	$000	$000	$0.00	0.00
MLTX02-004EN-763	Material Submittal for TrafficSigns	3.00	100%	100%	13 Apr 26	15Apr-26	13 Apr 26 A	15Apr-26A	$000	$000	$0.00	0.00
MLTX02-004EN-764	Material Approval forTrafficSigns	6.00	100%	100%	16 Apr 26	22Apr-26	16 Apr 26 A	22Apr-26A	$000	$000	$0.00	0.00
IRRGATIONPI PESSPRI NKLERS		9300	0%	0%	13 Apr 26	11Jul-26	13 Apr 26 A	27Jul-26A	$000	$000	$0.00	-1400
MLTX02-004EN-766	Material Submittal for Irrigation Pipes/Sprinkles	5.00	100%	100%	13 Apr 26	18Apr-26	13 Apr 26 A	18Apr-26A	$000	$000	$0.00	0.00
MLTX02-004EN-767	Material Approval forIrrigation Pipes/Sprinkles	6.00	100%	100%	05 Jul-26	11Jul-26	27 Jul-26	27Jul-26A	$000	$000	$0.00	5.00
AGRICULTURE SOIL		1400	0%	0%	06 May-26	21May-26	06 May 26 A	21May-26A	$000	$000	$0.00	0.00
MLTX02-004EN-769	Material Submittal for Agriculture Soil	1.00	100%	100%	06 May-26	06May-26	06 May 26 A	06May-26A	$000	$000	$0.00	0.00
MLTX02-004EN-770	Material Approval forAgriculture Soil	1.00	100%	100%	21 May-26	21May-26	21 May 26 A	21May-26A	$000	$000	$0.00	0.00
TRACK SURFACE		1400	0%	0%	06 May-26	21May-26	06 May 26 A	21May-26A	$000	$000	$0.00	0.00
MLTX02-004EN-772	Material Submittal for Track Suface	1.00	100%	100%	06 May-26	06May-26	06 May 26 A	06May-26A	$000	$000	$0.00	0.00
MLTX02-004EN-773	Material Approval forTrack Surface	1.00	100%	100%	21 May-26	21May-26	21 May 26 A	21May-26A	$000	$000	$0.00	0.00
GRASS/TREES		1400	0%	0%	06 May-26	21May-26	06 May 26 A	21May-26A	$000	$000	$0.00	0.00
MLTX02-004EN-775	Material Submittal for Grass/Trees	1.00	100%	100%	06 May-26	06May-26	06 May 26 A	06May-26A	$000	$000	$0.00	0.00
MLTX02-004EN-776	Material Approval forGrassTrees	1.00	100%	100%	21 May-26	21May-26	21 May 26 A	21May-26A	$000	$000	$0.00	0.00
CABLES		7.00	0%	0%	13 Apr 26	20Apr-26	13 Apr 26 A	20Apr-26A	$000	$000	$0.00	0.00
MLTX02-004EN-778	Material Submittal for Cables	5.00	100%	100%	13 Apr 26	18Apr-26	13 Apr 26 A	18Apr-26A	$000	$000	$0.00	0.00
MLTX02-004EN-779	Material Approval forCables	4.00	100%	100%	16 Apr 26	20Apr-26	16 Apr 26 A	20Apr-26A	$000	$000	$0.00	0.00
LIGHTPOLES		2100	0%	0%	13 Apr 26	06May-26	13 Apr 26 A	06May-26A	$000	$000	$0.00	0.00
MLTX02-004EN-781	Material Submittal for Lightingpoles	7.00	100%	100%	13 Apr 26	20Apr-26	13 Apr 26 A	20Apr-26A	$000	$000	$0.00	0.00
MLTX02-004EN-782	Material Approval forLightingpoles	1800	100%	100%	16 Apr 26	06May-26	16 Apr 26 A	06May-26A	$000	$000	$0.00	0.00
PROCU REMENT		25100	0%	0%	07 May-26	07Dec-26	07 May 26 A	07Feb-27	$000	$000	$0.00	-5300
SHORTEAD ITEM		22200	0%	0%	07 May-26	12Oct-26	07 May 26 A	25Jan-27	$000	$000	$0.00	-9000
TOILETSERVICE WORKS		16400	0%	0%	07 May-26	08Aug-26	07 May 26 A	18Nov-26	$000	$000	$0.00	-8700
STEELREINFORCEMENT		2400	0%	0%	13 May-26	13Jun-26	13 May 26 A	13Jun-26A	$000	$000	$0.00	0.00
MLTX02-004PR-7880	PO for Steel Reinforcement	2.00	100%	100%	13 May-26	14May-26	13 May 26 A	14May-26A	$000	$000	$0.00	0.00
MLTX02-004PR-7900	Material Delivery of SteelReinforcement	1.00	100%	100%	13 Jun 26	13Jun-26	13 Jun 26 A	13Jun-26A	$000	$000	$0.00	0.00
CONCRETE BLOCKS		7000	0%	0%	07 May-26	08Jul-26	07 May 26 A	27Jul-26A	$000	$000	$0.00	-1600
MLTX02-004PR-7950	PO for ConcreteBlocks	1.00	100%	100%	07 May-26	07May-26	07 May 26 A	07May-26A	$000	$000	$0.00	0.00
MLTX02-004PR-7970	Material Delivery ofConcrete Blocks	4.00	100%	100%	05 Jul-26	08Jul-26	27 Jul-26	27Jul-26A	$000	$000	$0.00	3.00
FLOORWALL TILES		7100	0%	0%	13 Jul-26	02Aug-26	27 Jul-26	12Sep-26A	$000	$000	$0.00	-2700
MLTX02-004PR-8030	PO for TilingMaterials	5.00	100%	100%	13 Jul-26	18Jul-26	27 Jul-26	22Jul-26A	$000	$000	$0.00	4.00
MLTX02-004PR-8050	Material Delivery ofTailingMaterial	1300	100%	100%	19 Jul-26	02Aug-26	12 Sep 26 A	12Sep-26A	$000	$000	$0.00	12.00
SUSPENDED CELING		8600	0%	0%	19 Jul-26	08Aug-26	27 Jul-26	10Oct-26A	$000	$000	$0.00	-4900
MLTX02-004PR-8070	PO for Suspend Celing	5.00	100%	100%	19 Jul-26	23Jul-26	27 Jul-26	22Jul-26A	$000	$000	$0.00	4.00
MLTX02-004PR-8090	Material Delivery ofSuspendCeiling	1300	100%	100%	25 Jul-26	08Aug-26	10 Oct 26 A	10Oct-26A	$000	$000	$0.00	13.00
DOORS/WINDO WS		11200	0%	0%	24 Jun 26	21Jul-26	24 Jun 26 A	03Oct-26A	$000	$000	$0.00	-6200
MLTX02-004PR-8110	PO for Doos/Windows	1.00	100%	100%	24 Jun 26	24Jun-26	24 Jun 26 A	24Jun-26A	$000	$000	$0.00	0.00
MLTX02-004PR-8130	Material Delivery for Doos/Windows	1500	100%	100%	05 Jul-26	21Jul-26	01 Oct 26 A	03Oct-26A	$000	$000	$0.00	13.00
WATERSUPPLYPIPES		1.00	0%	0%	13 Jun 26	13Jun-26	13 Jun 26 A	13Jun-26A	$000	$000	$0.00	0.00
MLTX02-004PR-8230	PO for Water Supply Pipes	1.00	100%	100%	13 Jun 26	13Jun-26	13 Jun 26 A	13Jun-26A	$000	$000	$0.00	0.00
MLTX02-004PR-8250	Material Delivery for Water Supply Pipes	1.00	100%	100%	13 Jun 26	13Jun-26	13 Jun 26 A	13Jun-26A	$000	$000	$0.00	0.00
SEWAGEDRAI NAGEPI PES		1.00	0%	0%	13 Jun 26	13Jun-26	13 Jun 26 A	13Jun-26A	$000	$000	$0.00	0.00
MLTX02-004PR-8270	PO for Sewage/Drainage Pipes	1.00	100%	100%	13 Jun 26	13Jun-26	13 Jun 26 A	13Jun-26A	$000	$000	$0.00	0.00
MLTX02-004PR-8290	Material Delivery for Sewage/Drainage Pipes	1.00	100%	100%	13 Jun 26	13Jun-26	13 Jun 26 A	13Jun-26A	$000	$000	$0.00	0.00
SANITARYFIXTURES		11700	0%	0%	16 Jun 26	19Jul-26	16 Jun 26 A	03Aug-26A	$000	$000	$0.00	-1300
MLTX02-004PR-8190	PO for SanitaryFixtures	1.00	100%	100%	16 Jun 26	16Jun-26	16 Jun 26 A	16Jun-26A	$000	$000	$0.00	0.00
MLTX02-004PR-8210	Material Delivery for SanitaryFixtures	1300	100%	100%	05 Jul-26	19Jul-26	08 Aug 26 A	03Aug-26A	$000	$000	$0.00	12.00
PACKAGE ACUNI TS		12800	0%	0%	16 Jun 26	21Jul-26	16 Jun 26 A	12Nov-26	$000	$000	$0.00	-9700
MLTX02-004PR-8330	Material Delivery for Package AC Units	1500	100%	0%	05 Jul-26	21Jul-26	27 Oct 26	12Nov-26	$000	$000	$0.00	0.00
MLTX02-004PR-8310	PO for Package AC Units	1.00	100%	100%	16 Jun 26	16Jun-26	16 Jun 26 A	16Jun-26A	$000	$000	$0.00	0.00
AIRDIFUSSERS/ GRILLS		11900	0%	0%	16 Jun 26	21Jul-26	16 Jun 26 A	08Aug-26A	$000	$000	$0.00	-1500
MLTX02-004PR-8350	PO for AirDiffusersGrills	1.00	100%	100%	16 Jun 26	16Jun-26	16 Jun 26 A	16Jun-26A	$000	$000	$0.00	0.00
MLTX02-004PR-8370	Material Delivery for AirDiffusersGrills	1500	100%	100%	05 Jul-26	21Jul-26	08 Aug 26 A	08Aug-26A	$000	$000	$0.00	14.00
GALVANIZED D UCTS		11900	0%	0%	16 Jun 26	21Jul-26	16 Jun 26 A	08Aug-26A	$000	$000	$0.00	-1500
MLTX02-004PR-8390	PO for GalvanizedDucts	1.00	100%	100%	16 Jun 26	16Jun-26	16 Jun 26 A	16Jun-26A	$000	$000	$0.00	0.00
MLTX02-004PR-8410	Material Delivery for GalvanizedDucts	1500	100%	100%	05 Jul-26	21Jul-26	08 Aug 26 A	08Aug-26A	$000	$000	$0.00	14.00
EXHAUSTFANS		11400	0%	0%	16 Jun 26	15Jul-26	16 Jun 26 A	17Aug-26A	$000	$000	$0.00	-2800
MLTX02-004PR-8430	PO for Exhaust Fans	1.00	100%	100%	16 Jun 26	16Jun-26	16 Jun 26 A	16Jun-26A	$000	$000	$0.00	0.00
MLTX02-004PR-8450	Material Delivery for Exhaust Fans	1000	100%	100%	05 Jul-26	15Jul-26	17 Aug 26 A	17Aug-26A	$000	$000	$0.00	9.00
LIGHTING FIXTURES		12300	0%	0%	16 Jun 26	15Jul-26	16 Jun 26 A	07Nov-26	$000	$000	$0.00	-9700

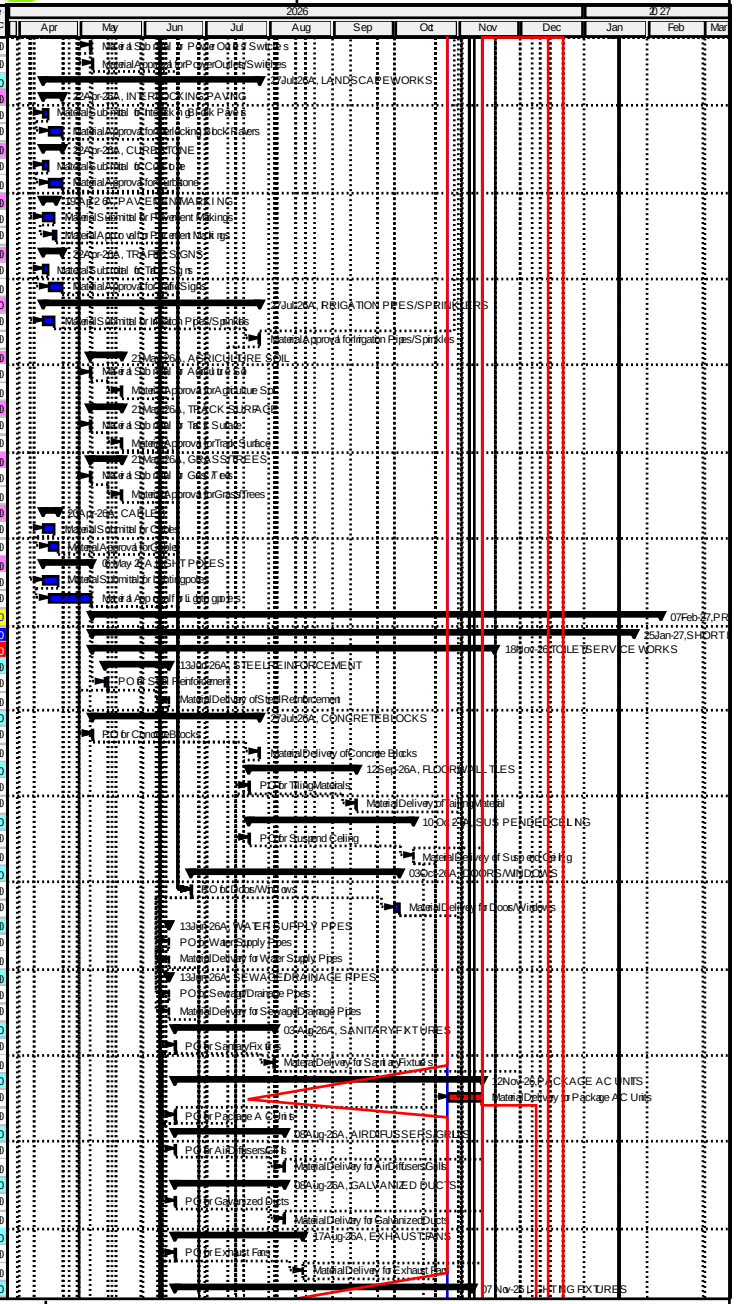


© Oracle Corporation

MLTX-02-004 - Playground Initiative for Western Region (Asir-Jazan -Jeddah)

Updateded schedule D.D 26-10-2026

ActivityID	ActivityName	Orginal Duration	Schedule %	Performance% Complete	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cos	Earned Value Cos	Budgeted Tot Cos	Variance BL Project
MLTX02.00.4PR-8490	Material Delivery for Lighting Fixtures	1000	100%	0%	05 Jul-25	15Jul-26	27 Oct 25	07Nov-26	$000	$000	$0.00	0.00
MLTX02.00.4PR-8470	PO for Lighting Fixtures	1.00	100%	100%	16 Jun 25	16Jun-26	16 Jun 25A	16Jun-26A	$000	$000	$0.00	0.00
SWITCHES/SOCKETS		11300	0%	0%	24 Jun 25	12Jul-26	24 Jun 25A	03Nov-26	$000	$000	$0.00	-9700
MLTX02.00.4PR-8530	Material Delivery for Switches/Sockets	7.00	100%	0%	05 Jul-25	12Jul-26	27 Oct 25	03Nov-26	$000	$000	$0.00	0.00
MLTX02.00.4PR-8510	PO for Switches/Sockets	1.00	100%	100%	24 Jun 25	24Jun-26	24 Jun 25A	24Jun-26A	$000	$000	$0.00	0.00
EARTHINGSYSTEM		1.00	0%	0%	21 May-26	21May-26	21 May 25 A	21May-26A	$000	$000	$0.00	0.00
MLTX02.00.4PR-8550	PO for EathingSystem	1.00	100%	100%	21 May-26	21May-26	21 May 25 A	21May-26A	$000	$000	$0.00	0.00
MLTX02.00.4PR-8570	Material Delivery for EarthingSystem	1.00	100%	100%	21 May-26	21May-26	21 May 25 A	21May-26A	$000	$000	$0.00	0.00
DISTRIBUTION PANNELS		9700	0%	0%	05 Jul-25	27Jul-26	22 Jul-26A	12Nov-26	$000	$000	$0.00	-7200
MLTX02.00.4PR-8610	Material Delivery for Distibution Panels	1500	100%	0%	11 Jul-25	27Jul-26	27 Oct 25	12Nov-26	$000	$000	$0.00	0.00
MLTX02.00.4PR-8590	PO for Distribution Panels	5.00	100%	100%	05 Jul-25	09Jul-26	22 Jul-26A	22Jul-26A	$000	$000	$0.00	4.00
FURNITURES		13300	0%	0%	16 Jun 25	27Jul-26	16 Jun 25A	18Nov-26	$000	$000	$0.00	-9700
MLTX02.00.4PR-8170	Material Delivery for Furnitures	2000	100%	0%	05 Jul-25	27Jul-26	27 Oct 25	18Nov-26	$000	$000	$0.00	0.00
MLTX02.00.4PR-8150	PO for Furnitures	1.00	100%	100%	16 Jun 25	16Jun-26	16 Jun 25A	16Jun-26A	$000	$000	$0.00	0.00
PLAYGROUND WORKS		17400	0%	0%	07 May-26	01Sep-26	07 May 25 A	30Nov-26	$000	$000	$0.00	-7600
PVC MEMBRANE		11700	0%	0%	16 Jun 25	08Jul-26	16 Jun 25A	31Oct-26	$000	$000	$0.00	-9700
MLTX02.00.4PR-8650	Material Delivery for PVC Membrane	4.00	100%	0%	05 Jul-25	08Jul-26	27 Oct 25	31Oct-26	$000	$000	$0.00	0.00
MLTX02.00.4PR-8640	PO for PVC Membrane	1.00	100%	100%	16 Jun 25	16Jun-26	16 Jun 25A	16Jun-26A	$000	$000	$0.00	0.00
ARTIFICIAL TURF		12900	0%	0%	16 Jun 25	22Jul-26	16 Jun 25A	14Nov-26	$000	$000	$0.00	-9700
MLTX02.00.4PR-8850	Material Delivery for Artificial TURF	1200	100%	0%	09 Jul-25	22Jul-26	01 Nov 25	14Nov-26	$000	$000	$0.00	0.00
MLTX02.00.4PR-8830	PO for Artificial TURF	1.00	100%	100%	16 Jun 25	16Jun-26	16 Jun 25A	16Jun-26A	$000	$000	$0.00	0.00
RUBBER GRANULES		4300	0%	0%	16 Jun 25	18Jul-26	16 Jun 25A	22Jul-26A	$000	$000	$0.00	-400
MLTX02.00.4PR-8870	PO for Rubber Granules	1.00	100%	100%	16 Jun 25	16Jun-26	16 Jun 25A	16Jun-26A	$000	$000	$0.00	0.00
MLTX02.00.4PR-8890	Material Delivery for Rubber Granules	1200	100%	100%	05 Jul-25	18Jul-26	22 Jul-26A	22Jul-26A	$000	$000	$0.00	11.00
PADEL GLASS		13100	0%	0%	16 Jun 25	25Jul-26	16 Jun 25A	16Nov-26	$000	$000	$0.00	-9700
MLTX02.00.4PR-8930	Material Delivery for PadelGlass	1800	100%	0%	05 Jul-25	25Jul-26	27 Oct 25	16Nov-26	$000	$000	$0.00	0.00
MLTX02.00.4PR-8910	PO for Padel Glass	1.00	100%	100%	16 Jun 25	16Jun-26	16 Jun 25A	16Jun-26A	$000	$000	$0.00	0.00
PADEL WIRE MESH/STEEL SETS		12900	0%	0%	16 Jun 25	22Jul-26	16 Jun 25A	14Nov-26	$000	$000	$0.00	-9700
MLTX02.00.4PR-8970	Material Delivery for Wire Mesh/Steel Sets	1600	100%	0%	05 Jul-25	22Jul-26	27 Oct 25	14Nov-26	$000	$000	$0.00	0.00
MLTX02.00.4PR-8950	PO for Wire Mesh/Steel Sets	1.00	100%	100%	16 Jun 25	16Jun-26	16 Jun 25A	16Jun-26A	$000	$000	$0.00	0.00
AGGREGATE BASECOURSE		1.00	0%	0%	21 May-26	21May-26	21 May 25 A	21May-26A	$000	$000	$0.00	0.00
MLTX02.00.4PR-8990	PO for AggregateBase Course	1.00	100%	100%	21 May-26	21May-26	21 May 25 A	21May-26A	$000	$000	$0.00	0.00
MLTX02.00.4PR-9000	Material Delivery for AggregateBase Course	1.00	100%	100%	21 May-26	21May-26	21 May 25 A	21May-26A	$000	$000	$0.00	0.00
BITUMINOUS BASE &WEARING COURSE		1.00	0%	0%	16 Jun 25	16Jun-26	16 Jun 25A	16Jun-26A	$000	$000	$0.00	0.00
MLTX02.00.4PR-9020	PO for BituminousBase &Wearing Course	1.00	100%	100%	16 Jun 25	16Jun-26	16 Jun 25A	16Jun-26A	$000	$000	$0.00	0.00
MLTX02.00.4PR-9030	Material Delivery for theSite	1.00	100%	100%	16 Jun 25	16Jun-26	16 Jun 25A	16Jun-26A	$000	$000	$0.00	0.00
INTERLOCKING PAVING		15100	0%	0%	07 May-26	12Jul-26	07 May 25 A	03Nov-26	$000	$000	$0.00	-9700
MLTX02.00.4PR-9070	Material Delivery for Interlocking Block Pavers	7.00	100%	0%	05 Jul-25	12Jul-26	27 Oct 25	03Nov-26	$000	$000	$0.00	0.00
MLTX02.00.4PR-9050	PO for InterlockingBlock Pavers	1.00	100%	100%	07 May-26	07May-26	07 May 25 A	07May-26A	$000	$000	$0.00	0.00
MARKING PAINT		9300	0%	0%	05 Jul-25	18Jul-26	18 Jul-26A	03Nov-26	$000	$000	$0.00	-8100
MLTX02.00.4PR-9110	Material Delivery for Marking Paint	7.00	100%	0%	11 Jul-25	18Jul-26	27 Oct 25	03Nov-26	$000	$000	$0.00	0.00
MLTX02.00.4PR-9090	PO for Making Paint	5.00	100%	100%	05 Jul-25	09Jul-26	18 Jul-26A	18Jul-26A	$000	$000	$0.00	4.00
PACKAGE ACUNITS		12800	0%	0%	16 Jun 25	21Jul-26	16 Jun 25A	12Nov-26	$000	$000	$0.00	-9700
MLTX02.00.4PR-9150	Material Delivery for Package AC Units	1500	100%	0%	05 Jul-25	21Jul-26	27 Oct 25	12Nov-26	$000	$000	$0.00	0.00
MLTX02.00.4PR-9130	PO for Package AC Units	1.00	100%	100%	16 Jun 25	16Jun-26	16 Jun 25A	16Jun-26A	$000	$000	$0.00	0.00
AIRDIFUSSERS/ GRILLS		11900	0%	0%	16 Jun 25	21Jul-26	16 Jun 25A	08Aug-26A	$000	$000	$0.00	-1500
MLTX02.00.4PR-9170	PO for AirDiffussers/Grills	1.00	100%	100%	16 Jun 25	16Jun-26	16 Jun 25A	16Jun-26A	$000	$000	$0.00	0.00
MLTX02.00.4PR-9190	Material Delivery for AirDifussers/Grills	1500	100%	100%	05 Jul-25	21Jul-26	08 Aug 25 A	08Aug-26A	$000	$000	$0.00	14.00
GALVANIZED D UCTS		11900	0%	0%	16 Jun 25	21Jul-26	16 Jun 25A	08Aug-26A	$000	$000	$0.00	-1500
MLTX02.00.4PR-9210	PO for GalvanizedDuct	1.00	100%	100%	16 Jun 25	16Jun-26	16 Jun 25A	16Jun-26A	$000	$000	$0.00	0.00
MLTX02.00.4PR-9230	Material Delivery for GalvanizedDuct	1500	100%	100%	05 Jul-25	21Jul-26	08 Aug 25 A	08Aug-26A	$000	$000	$0.00	14.00
EXHAUST FANS		11900	0%	0%	16 Jun 25	21Jul-26	16 Jun 25A	17Aug-26A	$000	$000	$0.00	-2300
MLTX02.00.4PR-9250	PO for Exhaust Fans	1.00	100%	100%	16 Jun 25	16Jun-26	16 Jun 25A	16Jun-26A	$000	$000	$0.00	0.00
MLTX02.00.4PR-9270	Material Delivery for Exhaust Fans	1500	100%	100%	05 Jul-25	21Jul-26	17 Aug 25 A	17Aug-26A	$000	$000	$0.00	14.00
DISTRBUTION BOARDS		8100	0%	0%	23 Jul-25	15Aug-26	22 Jul-26A	12Nov-26	$000	$000	$0.00	-7700
MLTX02.00.4PR-9310	Material Delivery for Distibution Boards	1500	100%	0%	29 Jul-25	15Aug-26	27 Oct 25	12Nov-26	$000	$000	$0.00	0.00
MLTX02.00.4PR-9290	PO for DistribuionBoards	5.00	100%	100%	23 Jul-25	28Jul-26	22 Jul-26A	22Jul-26A	$000	$000	$0.00	5.00
POWERCABLES		9200	0%	0%	29 Jul-25	15Aug-26	22 Jul-26A	07Nov-26	$000	$000	$0.00	-7700
MLTX02.00.4PR-9350	Material Delivery for PowerCables	1000	100%	0%	04 Aug-26	15Aug-26	27 Oct 25	07Nov-26	$000	$000	$0.00	0.00
MLTX02.00.4PR-9330	PO for PowerCables	5.00	100%	100%	29 Jul-25	03Aug-26	22 Jul-26A	22Jul-26A	$000	$000	$0.00	4.00
LIGHTFIXTURES		12900	0%	0%	16 Jun 25	22Jul-26	16 Jun 25A	14Nov-26	$000	$000	$0.00	-9700
MLTX02.00.4PR-9390	Material Delivery for Light Fixtures	1600	100%	0%	05 Jul-25	22Jul-26	27 Oct 25	14Nov-26	$000	$000	$0.00	0.00
MLTX02.00.4PR-9370	PO for Light Fixtures	1.00	100%	100%	16 Jun 25	16Jun-26	16 Jun 25A	16Jun-26A	$000	$000	$0.00	0.00
CCTV MATERIA IS		3000	0%	0%	12 Jul-25	01Sep-26	27 Oct 25	30Nov-26	$000	$000	$0.00	15.00
MLTX02.00.4PR-9410	PO for CCTV	5.00	100%	0%	12 Jul-25	16Jul-26	27 Oct 25	01Nov-26	$000	$000	$0.00	0.00
MLTX02.00.4PR-9430	Material Delivery for CCTV	1500	100%	0%	16 Aug-26	01Sep-26	14 Nov 25	30Nov-26	$000	$000	$0.00	0.00
POWEROUTLE TS/ SWITCHES		8200	0%	0%	22 Jul-25	15Aug-26	22 Jul-26A	12Nov-26	$000	$000	$0.00	-7600
MLTX02.00.4PR-9470	Material Delivery for PowerOutlets/Switches	1500	100%	0%	29 Jul-25	15Aug-26	27 Oct 25	12Nov-26	$000	$000	$0.00	0.00
MLTX02.00.4PR-9450	PO for PowerOutlets/Switches	6.00	100%	100%	22 Jul-25	28Jul-26	22 Jul-26A	22Jul-26A	$000	$000	$0.00	5.00
LANDSCAPE WORKS		22200	0%	0%	07 May-26	12Oct-26	07 May 25 A	25Jan-27	$000	$000	$0.00	-9000
INTERLOCKING PAVING		18600	0%	0%	07 May-26	15Sep-26	07 May 25 A	14Dec-26	$000	$000	$0.00	-7600
MLTX02.00.4PR-9520	Material Delivery for Interlocking Block Pavers	1200	100%	0%	02 Sep-26	15Sep-26	01 Dec 25	14Dec-26	$000	$000	$0.00	0.00

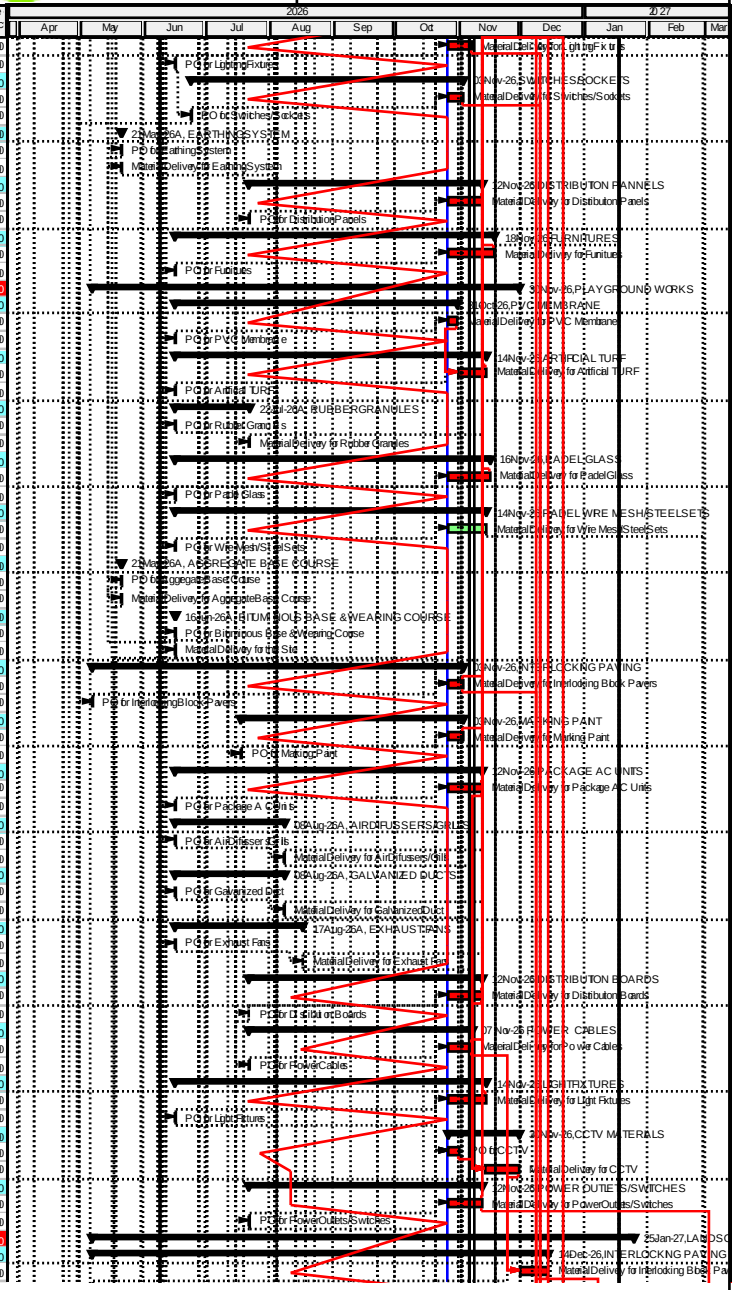


Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work

TASK filter: All Activities

© Oracle Corporation

ActivityID	ActivityName	Orginal Duration	Schedule %	Performance% Complete	BL Project Stat	BL Project Finish	Stat	Finish	Planned Value Cos	Earned Value Cos	Budgeted Tot Cos	Variance - BL Project
MLTX020 4PR-9500	PO for InterlockingBlock Pavers	1.0	100%	100%	07-May-26	07-May-26	07 May 26 A	07-May-26A	$000	$000	$0.0	0.0
CURBSTONE		11300	0%	0%	07-May-26	05-Aug-26	07 May 26 A	12-Aug-26A	$000	$000	$0.0	-600
MLTX020 4PR-9540	PO for Curbstone	1.0	100%	100%	07-May-26	07-May-26	07 May 26 A	07-May-26A	$000	$000	$0.0	0.0
MLTX020 4PR-9560	MaterialDelivery for Curbstone	1200	100%	100%	23-Jul-26	05-Aug-26	12-Aug-26 A	12-Aug-26A	$000	$000	$0.0	11.0
PAVEMENTMARKNG		6400	0%	0%	06-Aug-26	23-Aug-26	21-Jul-26A	07-Nov-26	$000	$000	$0.0	-7700
MLTX020 4PR-9600	MaterialDelivery for Pavement Makings	1000	100%	0%	12-Aug-26	23-Aug-26	27-Oct-26	07-Nov-26	$000	$000	$0.0	0.0
MLTX020 4PR-9580	PO for Pavement Makings	5.0	100%	100%	06-Aug-26	11-Aug-26	22-Jul-26A	22-Jul-26A	$000	$000	$0.0	4.0
TRAFFC SIGNS		1400	0%	0%	16-Sep-26	03-Oct-26	09-Jan-27	24-Jan-27	$000	$000	$0.0	0.0
MLTX020 4PR-9620	PO for TrafficSigns	5.0	100%	0%	16-Sep-26	21-Sep-26	09-Jan-27	13-Jan-27	$000	$000	$0.0	0.0
MLTX020 4PR-9640	MaterialDelivery for TrafficSigns	9.0	100%	0%	22-Sep-26	03-Oct-26	14-Jan-27	24-Jan-27	$000	$000	$0.0	0.0
IRRGATION PIPESSPRINKLERS		7200	0%	0%	12-Aug-26	26-Aug-26	18-Jul-26A	13-Aug-26A	$000	$000	$0.0	-1100
MLTX020 4PR-9660	PO for Irrigation Pipes/Sprinkles	5.0	100%	100%	12-Aug-26	17-Aug-26	18-Jul-26A	18-Jul-26A	$000	$000	$0.0	4.0
MLTX020 4PR-9680	MaterialDelivery for Irrigation Pipes/Sprinkles	8.0	100%	100%	18-Aug-26	26-Aug-26	13-Aug-26 A	13-Aug-26A	$000	$000	$0.0	7.0
AGRICULTURE SOL		8000	0%	0%	22-Sep-26	12-Oct-26	08-Aug-26 A	09-Nov-26	$000	$000	$0.0	-6300
MLTX020 4PR-9720	MaterialDelivery for Agriculture Sol	1200	100%	0%	29-Sep-26	12-Oct-26	27-Oct-26	09-Nov-26	$000	$000	$0.0	0.0
MLTX020 4PR-9700	PO for Agriculture Sol	5.0	100%	100%	22-Sep-26	28-Sep-26	08-Aug-26 A	08-Aug-26A	$000	$000	$0.0	4.0
TRACK SURFACE		1500	0%	0%	05-Sep-26	21-Sep-26	28-Dec-26	13-Jan-27	$000	$000	$0.0	0.0
MLTX020 4PR-9740	PO for Track Suface	5.0	100%	0%	05-Sep-26	09-Sep-26	28-Dec-26	02-Jan-27	$000	$000	$0.0	0.0
MLTX020 4PR-9760	MaterialDelivery for Track Surface	1000	100%	0%	10-Sep-26	21-Sep-26	03-Jan-27	13-Jan-27	$000	$000	$0.0	0.0
GRASS/TREES		2000	0%	0%	10-Sep-26	04-Oct-26	08-Jan-27	25-Jan-27	$000	$000	$0.0	0.0
MLTX020 4PR-9780	PO for Grass/Trees	5.0	100%	0%	10-Sep-26	15-Sep-26	03-Jan-27	07-Jan-27	$000	$000	$0.0	0.0
MLTX020 4PR-9800	MaterialDelivery for Grass/Trees	1500	100%	0%	16-Sep-26	04-Oct-26	09-Jan-27	25-Jan-27	$000	$000	$0.0	0.0
CABLES		2000	0%	0%	12-Aug-26	03-Sep-26	28-Sep-26 A	28-Sep-26A	$000	$000	$0.0	19.0
MLTX020 4PR-9820	PO for Cables	5.0	100%	100%	12-Aug-26	17-Aug-26	28-Sep-26 A	28-Sep-26A	$000	$000	$0.0	4.0
MLTX020 4PR-9840	MaterialDelivery for Cables	1500	100%	100%	18-Aug-26	03-Sep-26	28-Sep-26 A	28-Sep-26A	$000	$000	$0.0	14.0
LONG LEAD ITEM		22000	0%	0%	16-Jun-26	07-Dec-26	16-Jun-26A	07-Feb-27	$000	$000	$0.0	-5300
PLAYGROUND WORKS		20200	0%	0%	16-Jun-26	17-Oct-26	16-Jun-26A	07-Feb-27	$000	$000	$0.0	-9700
STEELTENSION CABLES		20200	0%	0%	16-Jun-26	17-Oct-26	16-Jun-26A	07-Feb-27	$000	$000	$0.0	-9700
MLTX020 4PR-8690	MaterialDelivery for Steel Tension Cables	2900	100%	0%	05-Sep-26	08-Oct-26	28-Dec-26	30-Jan-27	$000	$000	$0.0	0.0
MLTX020 4PR-8680	MaterialFabricationforSteelTension Cables	2000	100%	0%	29-Jul-26	20-Aug-26	27-Oct-26	18-Nov-26	$000	$000	$0.0	0.0
MLTX020 4PR-9890	Staging time	7.0	100%	0%	10-Oct-26	17-Oct-26	31-Jan-27	07-Feb-27	$000	$000	$0.0	0.0
MLTX020 4PR-8670	PO for Steel Tension Cables	1.0	100%	100%	16-Jun-26	16-Jun-26	16-Jun-26 A	16-Jun-26A	$000	$000	$0.0	0.0
EMERGENCY DOORS		16600	0%	0%	16-Jun-26	03-Sep-26	16-Jun-26A	27-Dec-26	$000	$000	$0.0	-9700
MLTX020 4PR-8730	MaterialDelivery for Emergency Doors	2500	100%	0%	28-Jul-26	25-Aug-26	19-Nov-26	17-Dec-26	$000	$000	$0.0	0.0
MLTX020 4PR-8720	MaterialFabricationforEmergency Doos	2000	100%	0%	05-Jul-26	27-Jul-26	27-Oct-26	18-Nov-26	$000	$000	$0.0	0.0
MLTX020 4PR-9900	Staging time	8.0	100%	0%	26-Aug-26	03-Sep-26	19-Dec-26	27-Dec-26	$000	$000	$0.0	0.0
MLTX020 4PR-8710	PO for Emegency Doors	1.0	100%	100%	16-Jun-26	16-Jun-26	16-Jun-26 A	16-Jun-26A	$000	$000	$0.0	0.0
PRESSURE UNITS		16600	0%	0%	16-Jun-26	03-Sep-26	16-Jun-26A	27-Dec-26	$000	$000	$0.0	-9700
MLTX020 4PR-8770	MaterialDelivery for Pressure Units	2500	100%	0%	28-Jul-26	25-Aug-26	19-Nov-26	17-Dec-26	$000	$000	$0.0	0.0
MLTX020 4PR-8760	MaterialFabricationforPressue Units	2000	100%	0%	05-Jul-26	27-Jul-26	27-Oct-26	18-Nov-26	$000	$000	$0.0	0.0
MLTX020 4PR-9910	Staging time	8.0	100%	0%	26-Aug-26	03-Sep-26	19-Dec-26	27-Dec-26	$000	$000	$0.0	0.0
MLTX020 4PR-8750	PO for PressureUnits	1.0	100%	100%	16-Jun-26	16-Jun-26	16-Jun-26 A	16-Jun-26A	$000	$000	$0.0	0.0
AIRLOCK DOORS		16600	0%	0%	16-Jun-26	03-Sep-26	16-Jun-26A	27-Dec-26	$000	$000	$0.0	-9700
MLTX020 4PR-8810	MaterialDelivery for LockDoors	2500	100%	0%	28-Jul-26	25-Aug-26	19-Nov-26	17-Dec-26	$000	$000	$0.0	0.0
MLTX020 4PR-8800	MaterialFabricationforLock Doors	2000	100%	0%	05-Jul-26	27-Jul-26	27-Oct-26	18-Nov-26	$000	$000	$0.0	0.0
MLTX020 4PR-9920	Staging time	8.0	100%	0%	26-Aug-26	03-Sep-26	19-Dec-26	27-Dec-26	$000	$000	$0.0	0.0
MLTX020 4PR-8790	PO for Lock Doors	1.0	100%	100%	16-Jun-26	16-Jun-26	16-Jun-26 A	16-Jun-26A	$000	$000	$0.0	0.0
LANDSCAPE WORKS		21800	0%	0%	18-Jun-26	07-Dec-26	18-Jun-26A	29-Sep-26A	$000	$000	$0.0	59.0
LIGHTPOLES		21800	0%	0%	18-Jun-26	07-Dec-26	18-Jun-26A	29-Sep-26A	$000	$000	$0.0	59.0
MLTX020 4PR-9860	PO for Lightingpoles	1.0	100%	100%	18-Jun-26	18-Jun-26	18-Jun-26 A	18-Jun-26A	$000	$000	$0.0	0.0
MLTX020 4PR-9870	MaterialFabricationforLighting pdes	3000	100%	100%	16-Sep-26	21-Oct-26	29-Sep-26 A	29-Sep-26A	$000	$000	$0.0	29.0
MLTX020 4PR-9880	MaterialDelivery for Lightingpoles	2500	15%	100%	22-Oct-26	19-Nov-26	29-Sep-26 A	29-Sep-26A	$000	$000	$0.0	24.0
MLTX020 4PR-9930	Staging time	1500	0%	100%	21-Nov-26	07-Dec-26	29-Sep-26 A	29-Sep-26A	$000	$000	$0.0	14.0
CONSTR UCTION PHASE		29600	3444%	3966%	27-Apr-26	24-Jan-27	27-Apr-26A	15-Apr-27	$3643.21382	$4194.75730	$10578.07300	-6600
SITEWORKS		29600	2612%	3934%	27-Apr-26	24-Jan-27	27-Apr-26A	15-Apr-27	$2441.59900	$3676.56738	$9366.37454	-6600
EARTH WORKS		8907	100%	100%	27-Apr-26	09-Aug-26	27-Apr-26A	12-Aug-26A	$1876.45721	$4876.45721	$4876.45721	-296
MLTX-02-004CN-9930	Excavation(inall types of soil)including Compaction(PlaygoundArea)	1275	100%	100%	27-Apr-26	11-May-26	27-Apr-26A	11-May-26A	$101400.00	$101400.00	$101400.00	0.0
MLTX-02-004CN-9940	Excavation(inall types of soil)including Compaction(Service/ToiletBuilding)	804	100%	100%	06-May-26	16-May-26	06-May-26 A	16-May-26A	$32321.25	$32321.25	$32321.25	0.0
MLTX-02-004CN-9950	Excavation(inall types of soil)including Compaction(Landscape Area)	1735	100%	100%	29-Apr-26	19-May-26	29-Apr-26A	19-May-26A	$209327.63	$209327.63	$209327.63	0.0
MLTX-02-004CN-9960	Backfilling onLayers(Selected Soil)including Compaction (Playground Area)	2040	100%	100%	17-May-26	13-Jun-26	17-May-26 A	13-Jun-26A	$61425.00	$61425.00	$61425.00	0.0
MLTX-02-004CN-9970	Backfilling onLayers(Selected Soil)including Compaction (Service/ToiletBuilding)	1780	100%	100%	17-May-26	09-Jun-26	17-May-26 A	09-Jun-26A	$17062.50	$17062.50	$17062.50	0.0
MLTX-02-004CN-9980	Backfilling onLayers(Selected Soil)including Compaction (LandscapeArea)	2300	100%	100%	08-Jun-26	04-Jul-26	08-Jun-26 A	04-Jul-26A	$29859.38	$29859.38	$29859.38	0.0
MLTX-02-004CN-9980R	Backfilling onLayers(Selected Soil)including Compaction (LandscapeArea)Remain	3007	100%	100%	05-Jul-26	09-Aug-26	04-Jul-26A	12-Aug-26A	$36249.96	$36249.96	$36249.96	-396
LANDSCAPE WORKS		27400	2206%	36%	23-May-26	24-Jan-27	23-May-26 A	15-Apr-27	$1953.95228	$3188.92167	$8858.72833	-6600
PLAYGROUND AREA		25800	4215%	4677%	23-May-26	04-Jan-27	23-May-26 A	28-Mar-27	$1801.55000	$5328.86225	$11392.25000	-6700
FOOTBALLPLAYGROUND		25000	20%	20%	23-May-26	13-Dec-26	23-May-26 A	18-Mar-27	$5152.50000	$5152.50000	$32876.25000	-7800
MLTX-02-004CN-100	FinishingandSurfaceFinish Woks (footbal Playground)	3000	0%	0%	29-Oct-26	02-Dec-26	27-Oct-26	30-Nov-26	$000	$000	$14812.50	0.0
MLTX-02-004CN-100	InstallSportEquipments -Goal /Nets- Footbal Playground)	9.0	0%	0%	03-Dec-26	13-Dec-26	06-Mar-27	18-Mar-27	$000	$000	$71906.25	0.0
MLTX-02-004CN-100	Surface Makingand Painting(FoobalPlaygound)	8.0	0%	0%	03-Dec-26	12-Dec-26	06-Mar-27	17-Mar-27	$000	$000	$14381.25	0.0
MLTX-02-004CN-100	Preparation andProofing for Subgade (Footbal Playgound)	1.2	100%	100%	23-May-26	24-May-26	23-May-26 A	24-May-26A	$2876.25	$2876.25	$28762.50	0.0
MLTX-02-004CN-100	Backfilling andCompacton ofBaseLayers(FoobalPlaygound)	3240	100%	100%	24-May-26	04-Jul-26	24-May-26 A	04-Jul-26A	$2444.813	$2444.813	$24448.13	0.0
MLTX-02-004CN-100	Backfilling andCompacton ofBaseLayers(FoobalPlaygound)Remaining	3000	100%	100%	05-Jul-26	08-Aug-26	20-Jul-26A	31-Aug-26A	$1314.38	$4314.38	$4314.38	-670

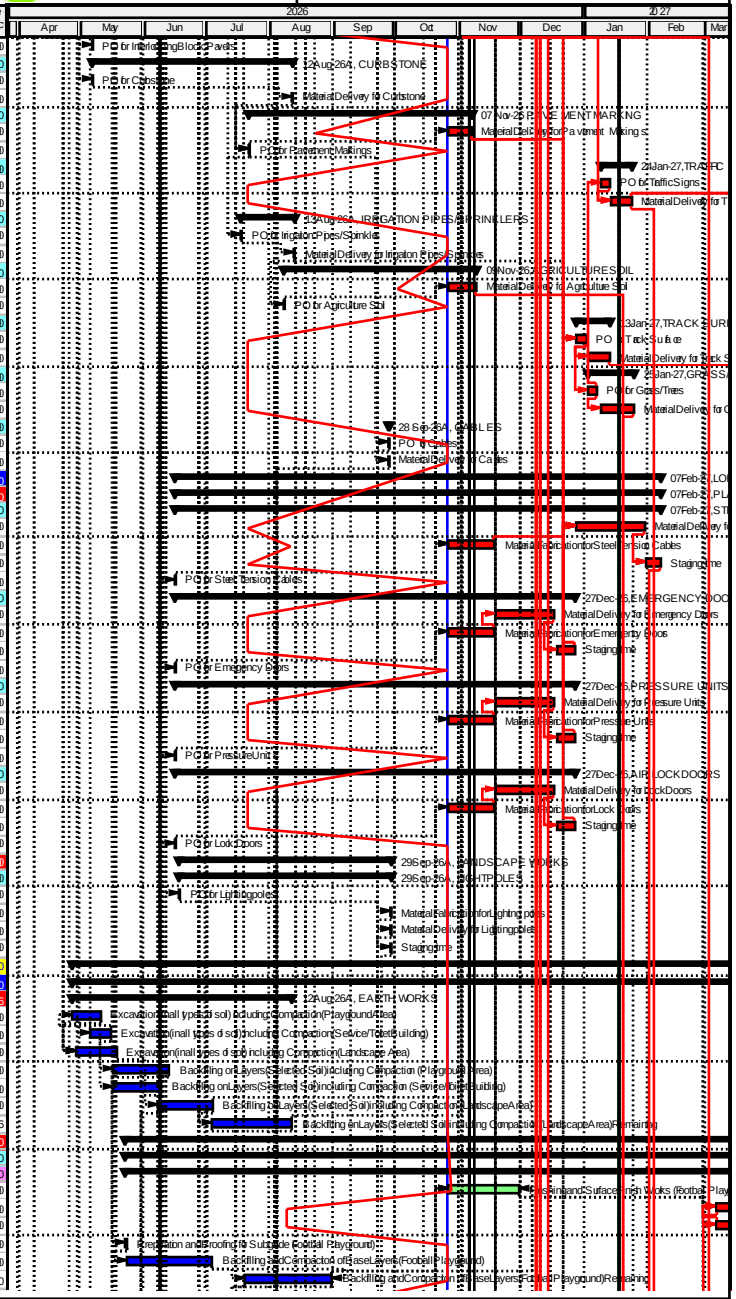


Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work

TASK filter: All Activities

© Oracle Corporation

ActivityID	ActivityName	Orginal Duration	Schedule %	Performance% Complete	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Variance - BL Project
PADEL PLAYGROUND		25100	5%	80%	23-May-26	14-Dec-26	23-May-26 A	20-Mar-27	$1,179,750.00	$171,600.00	$2,145,000.00	-7800
MLTX-02-004-CN-101	Install Sport Equipments -Goal /Nets- (Padel Playground)	1000	0%	0%	03-Dec-26	14-Dec-26	06-Mar-27	20-Mar-27	$0.00	$0.00	$32,175.00	0.00
MLTX-02-004-CN-101	Surface Making and Painting (Padel Playground)	800	0%	0%	03-Dec-26	12-Dec-26	08-Mar-27	20-Mar-27	$0.00	$0.00	$10,725.00	0.00
MLTX-02-004-CN-100	Preparation and Proofing for Subgrade (Padel Playground)	100	100%	100%	23-May-26	23-May-26	23-May-26 A	23-May-26A	$57,507.50	$57,507.50	$75,075.00	0.00
MLTX-02-004-CN-100	Backfilling and Compacton of Base Layers (Padel Playground)	3240	100%	100%	24-May-26	04-Jul-26	24-May-26 A	04-Jul-26A	$33,753.75	$28,758.75	$37,537.50	0.00
MLTX-02-004-CN-100	Finishing and Surface Finish Works (Padel Playground)	3000	0%	100%	29-Oct-26	02-Dec-26	15-Sep-26 A	16-Sep-26A	$0.00	$5,362.50	$53,625.00	29.00
MLTX-02-004-CN-100	Backfilling and Compacton of Base Layers (Padel Playground) Remaining	3000	100%	100%	09-Aug-26	12-Sep-26	20-Jul-26A	09-Aug-26A	$5,362.50	$5,362.50	$5,362.50	12.00
BASKETBALL PLAYGROUND		25800	1995%	6998%	23-May-26	20-Dec-26	23-May-26 A	28-Mar-27	$6,220.50	$218,205.00	$3,118,650.00	-8000
MLTX-02-004-CN-102	Install Sport Equipments -Goal /Nets- (Basketball Playground)	1500	0%	0%	03-Dec-26	20-Dec-26	06-Mar-27	25-Mar-27	$0.00	$0.00	$78,000.00	0.00
MLTX-02-004-CN-102	Surface Making and Painting (Basketball Playground)	700	0%	0%	13-Dec-26	20-Dec-26	21-Mar-27	28-Mar-27	$0.00	$0.00	$15,600.00	0.00
MLTX-02-004-CN-101	Backfilling and Compacton Subgrade (Basketball Playground)	600	100%	100%	23-May-26	23-May-26	23-May-26 A	23-May-26A	$3,120.00	$3,120.00	$31,200.00	0.00
MLTX-02-004-CN-101	Backfilling and Compacton of Base Layers (Basketball Playground)	3240	100%	100%	24-May-26	04-Jul-26	24-May-26 A	04-Jul-26A	$2,749.50	$2,749.50	$27,495.00	0.00
MLTX-02-004-CN-102	Finishing and Surface Finish Works (Basketball Playground)	3000	0%	100%	29-Oct-26	02-Dec-26	15-Sep-26 A	16-Sep-26A	$0.00	$15,600.00	$156,000.00	28.00
MLTX-02-004-CN-101	Backfilling and Compacton of Base Layers (Basketball Playground) Remaining	3000	100%	100%	13-Sep-26	18-Oct-26	20-Jul-26A	09-Aug-26A	$351.00	$351.00	$3,510.00	12.00
PADEL FENCE		16900	0%	35%	21-Dec-26	04-Jan-27	16-Aug-26 A	18-Nov-26	$0.00	$2,900.63	$82,875.00	-6800
MLTX-02-004-CN-102	Tempered Glass Fence Installation and Fixation	200	0%	0%	31-Dec-26	02-Jan-27	15-Nov-26	16-Nov-26	$0.00	$0.00	$33,150.00	0.00
MLTX-02-004-CN-102	Chain Link Fence Installation and Fixation	200	0%	0%	03-Jan-27	04-Jan-27	17-Nov-26	18-Nov-26	$0.00	$0.00	$16,575.00	0.00
MLTX-02-004-CN-102	Install of Fence Gates	200	0%	0%	03-Jan-27	04-Jan-27	17-Nov-26	18-Nov-26	$0.00	$0.00	$4,143.75	0.00
MLTX-02-004-CN-102	Excavation for Fence	500	0%	100%	21-Dec-26	26-Dec-26	16-Aug-26 A	16-Aug-26A	$0.00	$8,287.50	$8,287.50	4.00
MLTX-02-004-CN-102	Concrete Foundation for Fence including Posts Fixation	500	0%	100%	21-Dec-26	26-Dec-26	25-Aug-26 A	01-Sep-26A	$0.00	$1,657.50	$16,575.00	-200
MLTX-02-004-CN-102	Backfilling and Reinstatement for Concrete Foundation	400	0%	100%	27-Dec-26	30-Dec-26	08-Oct-26 A	08-Oct-26A	$0.00	$4,143.75	$4,143.75	3.00
CURBSTONE/INTERLOCK		10196	100%	2332%	23-Aug-26	22-Oct-26	10-Aug-26 A	26-Dec-26	$2,424,150.00	$56,650.00	$2,424,150.00	-6596
MLTX-02-004-CN-101	Interlock Installaton (Grey Scale) for Land Scape (Including Finishing Works)	1000	100%	0%	12-Oct-26	22-Oct-26	15-Dec-26	26-Dec-26	$1,859,000.00	$0.00	$1,859,000.00	0.00
MLTX-02-004-CN-101	Concrete Works Under Curbstone	1500	100%	100%	23-Aug-26	08-Sep-26	10-Aug-26 A	10-Aug-26A	$1,998,750.00	$1,998,750.00	$19,987.50	15.00
MLTX-02-004-CN-101	Curbstone Instalation	400	100%	100%	07-Oct-26	11-Oct-26	11-Aug-26 A	16-Aug-26A	$356,250.00	$56,650.00	$36,562.50	-100
AIRDOME		24800	1776%	278%	16-Jun-26	31-Dec-26	16-Jun-26 A	06-Apr-27	$9,954,801.56	$1,558,537.50	$5,606,250.00	-7800
CIVIL WORKS		21600	4228%	5524%	16-Jun-26	24-Nov-26	16-Jun-26 A	24-Feb-27	$9,954,801.56	$1,300,650.00	$2,354,625.00	-7800
MLTX-02-004-CN-103	Install of Membrane Covering System (Air Dome)	1400	0%	0%	09-Nov-26	24-Nov-26	08-Feb-27	24-Feb-27	$0.00	$0.00	$56,062.50	0.00
MLTX-02-004-CN-103	Thermal Insulation Works (Air Dome)	1400	12%	09-Nov-26	24-Nov-26	21-Oct-26 A	24-Feb-27	$0.00	$6,772.50	$56,062.50	-9400	
MLTX-02-004-CN-103	Excavation for Foundaiton & Playgound Area (Air Dome)	1150	100%	100%	16-Jun-26	29-Jun-26	16-Jun-26 A	29-Jun-26A	$2,803,125.00	$2,803,125.00	$2,803,125.00	0.00
MLTX-02-004-CN-103	Concrete Works for Foundations including Anchor Bolts (Air Dome)	2600	100%	100%	23-Jul-26	22-Aug-26	11-Jul-26A	22-Sep-26A	$3,924,375.00	$392,437.50	$3,924,375.00	-3744
MLTX-02-004-CN-103	Cable System Installaton (Air Dome)	1000	80%	100%	18-Oct-26	28-Oct-26	21-Sep-26 A	12-Oct-26A	$2,227,305.56	$560,625.00	$5,606,250.00	-600
MECHANICAL WORKS		1300	0%	0%	25-Nov-26	09-Dec-26	25-Feb-27	15-Mar-27	$0.00	$0.00	$1,121,250.00	0.00
MLTX-02-004-CN-104	Air Ducts and Grills Instalation (Air Dome)	1000	0%	0%	25-Nov-26	06-Dec-26	25-Feb-27	08-Mar-27	$0.00	$0.00	$2,803,125.00	0.00
MLTX-02-004-CN-104	Air Units Installaton (Air Dome)	1300	0%	0%	25-Nov-26	09-Dec-26	25-Feb-27	15-Mar-27	$0.00	$0.00	$4,485,000.00	0.00
MLTX-02-004-CN-104	Exhaust Fans and Ducts Instalation (Air Dome)	700	0%	0%	25-Nov-26	02-Dec-26	25-Feb-27	04-Mar-27	$0.00	$0.00	$3,924,375.00	0.00
ELECTRICAL WORKS		3200	0%	1533%	10-Dec-26	31-Dec-26	07-Oct-26 A	06-Apr-27	$0.00	$257,887.50	$1,681,875.00	-133.00
MLTX-02-004-CN-104	Distibuton Board and Electical Works (Air Dome)	300	0%	0%	15-Dec-26	17-Dec-26	16-Mar-27	18-Mar-27	$0.00	$0.00	$2,803,125.00	0.00
MLTX-02-004-CN-104	External Electical Connection Works (Air Dome)	400	0%	0%	19-Dec-26	22-Dec-26	20-Mar-27	23-Mar-27	$0.00	$0.00	$2,803,125.00	0.00
MLTX-02-004-CN-104	Emergency Gererator Installaton (Air Dome)	400	0%	0%	23-Dec-26	27-Dec-26	24-Mar-27	28-Mar-27	$0.00	$0.00	$5,606,250.00	0.00
MLTX-02-004-CN-104	Contol System Installaton (Air Dome)	400	0%	0%	28-Dec-26	31-Dec-26	01-Apr-27	06-Apr-27	$0.00	$0.00	$2,803,125.00	0.00
MLTX-02-004-CN-104	Light Fixture Works (Air Dome)	400	0%	92%	10-Dec-26	14-Dec-26	07-Oct-26 A	15-Mar-27	$0.00	$257,887.50	$2,803,125.00	-129.00
FINISHES WORKS		1500	0%	0%	10-Dec-26	27-Dec-26	16-Mar-27	01-Apr-27	$0.00	$0.00	$4,485,000.00	0.00
MLTX-02-004-CN-103	Doors Installaton including Emegency, Entrance doors (Air Dome)	600	0%	0%	10-Dec-26	16-Dec-26	16-Mar-27	22-Mar-27	$0.00	$0.00	$2,242,500.00	0.00
MLTX-02-004-CN-103	Logoand Signs Installaton (Air Dome)	900	0%	0%	17-Dec-26	27-Dec-26	23-Mar-27	01-Apr-27	$0.00	$0.00	$2,242,500.00	0.00
IRRIGATION NETWORK		10900	8504%	8203%	12-Oct-26	04-Nov-26	20-Aug-26 A	28-Jan-27	$2,624,137.50	$253,142.50	$3,085,875.00	-117.00
MLTX-02-004-CN-11460	Installing of Bubblers and Sprayers	300	0%	0%	02-Nov-26	04-Nov-26	25-Jan-27	28-Jan-27	$0.00	$0.00	$46,150.00	0.00
MLTX-02-004-CN-11450	Installing of Valves and fittings for Irigation Network	400	100%	80%	21-Oct-26	25-Oct-26	21-Sep-26 A	21-Dec-26	$4,647.50	$28,710.00	$46,475.00	-7200
MLTX-02-004-CN-11430	Installing of HDPE Pipes for Irrigation Network (Main Line)	400	100%	100%	12-Oct-26	15-Oct-26	20-Aug-26 A	29-Aug-26A	$10,725.00	$107,250.00	$107,250.00	-400
MLTX-02-004-CN-11440	Installing of HDPE Pipes for Irrigation Network (Branch Lines)	400	100%	100%	17-Oct-26	20-Oct-26	29-Aug-26 A	31-Aug-26A	$10,697.25	$10,871.25	$10,871.25	2.00
NATURAL GROUND		600	1667%	0%	26-Oct-26	01-Nov-26	27-Dec-26	02-Jan-27	$1,338,188.00	$0.00	$80,291.25	0.00
MLTX-02-004-10550	Compacted Natural Ground Soil Installation Works for Landscape	600	1667%	0%	26-Oct-26	01-Nov-26	27-Dec-26	02-Jan-27	$1,338,188.00	$0.00	$80,291.25	0.00
PLANTING		4600	0%	1154%	05-Nov-26	13-Dec-26	13-Oct-26 A	18-Mar-27	$0.00	$6,897.54	$5,978,375.00	-9800
MLTX-02-004-10580	Placement of Lawn Ground Cover (Rolling and Compacton)	300	0%	0%	10-Dec-26	13-Dec-26	16-Mar-27	18-Mar-27	$0.00	$0.00	$1,751,250.00	0.00
MLTX-02-004-10590	Placement and Fixation of Tees	300	0%	0%	07-Dec-26	09-Dec-26	09-Mar-27	15-Mar-27	$0.00	$0.00	$2,362,425.00	0.00
MLTX-02-004-10570	Placement of Sweet Agricultual Soil (Including Levelling and Grading)	300	0%	37%	05-Nov-26	08-Nov-26	13-Oct-26 A	28-Jan-27	$0.00	$6,897.54	$1,864,200.00	-9000
WALKING/BIKE PATHS		1200	0%	50%	14-Dec-26	27-Dec-26	11-Aug-26 A	18-Mar-27	$0.00	$138,206.39	$2,764,127.70	-172.00
MLTX-02-004-10510	Bike Path Preparation and Installation Works	1200	0%	50%	14-Dec-26	27-Dec-26	11-Aug-26 A	18-Mar-27	$0.00	$71,102.26	$1,420,456.36	-172.00
MLTX-02-004-10520	Walking Path Preparaton and Installation Works	1200	0%	50%	14-Dec-26	27-Dec-26	11-Aug-26 A	18-Mar-27	$0.00	$67,103.70	$1,343,671.41	-172.00
GENERAL/FURNITURE		14600	2382%	7495%	12-Oct-26	24-Jan-27	29-Sep-26 A	15-Apr-27	$2,024,197.75	$637,173.63	$8,500,918.81	-7700
MLTX-02-004-10610	Stamped Concete Works for Land Scape (Including Finishing Works)	900	0%	0%	28-Dec-26	06-Jan-27	20-Mar-27	29-Mar-27	$0.00	$0.00	$42,068.52	0.00
MLTX-02-004-10630	Fixation and Installation of Steel Frame for Benches	700	0%	0%	28-Dec-26	04-Jan-27	20-Mar-27	27-Mar-27	$0.00	$0.00	$17,276.03	0.00
MLTX-02-004-10640	Fixation and Installation of Benches	700	0%	0%	05-Jan-27	12-Jan-27	28-Mar-27	04-Apr-27	$0.00	$0.00	$40,310.72	0.00
MLTX-02-004-10650	Fixation and Installation of Pecast Concrete Seats (Rectangular)	700	0%	0%	05-Jan-27	12-Jan-27	28-Mar-27	04-Apr-27	$0.00	$0.00	$43,680.00	0.00
MLTX-02-004-10660	Fixation and Installation of Pecast Concrete Seats (Circular)	800	0%	0%	05-Jan-27	13-Jan-27	28-Mar-27	05-Apr-27	$0.00	$0.00	$17,160.00	0.00
MLTX-02-004-10670	Fixation and Installation of Pecast Concrete Trash Bins	900	0%	0%	14-Jan-27	24-Jan-27	06-Apr-27	15-Apr-27	$0.00	$0.00	$14,625.00	0.00
MLTX-02-004-11800	Installing of Site Light Poles	1100	0%	92%	07-Jan-27	19-Jan-27	01-Oct-26 A	29-Mar-27	$0.00	$434,675.88	$4,724,737.75	-139.00
MLTX-02-004-11710	Preliminary Works for Site Light Poles Including Cableand Bases Works	1200	100%	100%	12-Oct-26	25-Oct-26	29-Sep-26 A	01-Oct-26A	$2,024,197.75	$202,497.75	$2,024,197.75	9.00
TOILETS/SERVICE BULDING		18084	9756%	4207%	06-Jun-26	02-Nov-26	06-Jun-26 A	03-Jan-27	$1,201,615.25	$518,189.91	$1,231,705.41	-5300
STRUCTURE WORKS		6084	100%	100%	06-Jun-26	18-Aug-26	06-Jun-26 A	26-Jul-26A	$1,590,216.66	$158,021.66	$1,590,216.66	20.00
CONCRETE WORKS		5360	100%	100%	14-Jun-26	18-Aug-26	14-Jun-26 A	26-Jul-26A	$1,137,825.00	$113,782.50	$1,137,825.00	20.00
SUB-STRUCTURE		840	100%	100%	14-Jun-26	23-Jun-26	14-Jun-26 A	23-Jun-26A	$33,345.00	$33,345.00	$33,345.00	0.00

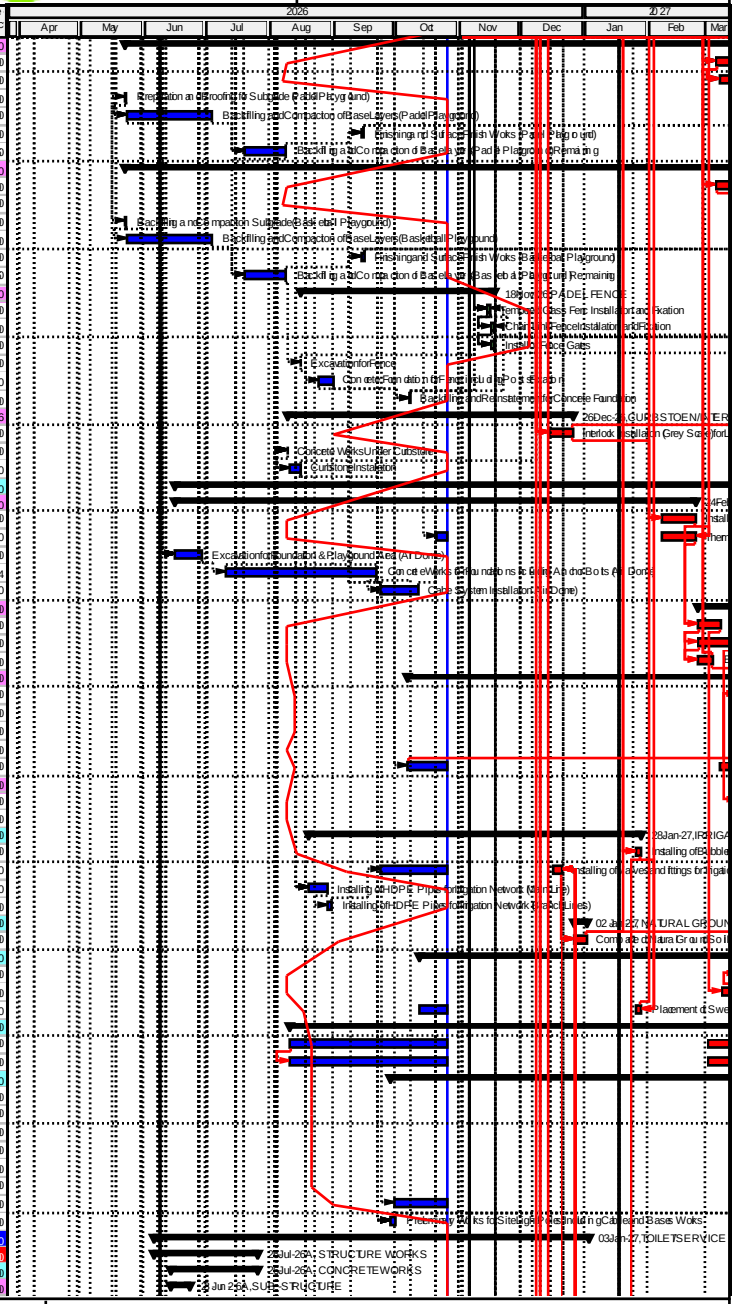


Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work

TASK filter: All Activities


© Oracle Corporation

ActivityID	ActivityName	Orginal Duration	Schedule %	Performance% Complete	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Variance - BL Project
MLTX02-004CN-107	Plain Concrete Under Footing	2.00	100%	100%	14-Jun-26	16-Jun-26	14-Jun-26A	16-Jun-26A	$1,170.00	$1,170.00	$1,170.00	0.00
MLTX02-004CN-108	ReinforcedConcrete Works for Slab onGrade Including Steel Fixing	7.20	100%	100%	15-Jun-26	23-Jun-26	15-Jun-26A	23-Jun-26A	$32,175.00	$32,175.00	$32,175.00	0.00
SUPER-STRUCTURE		1900	100%	100%	15-Jul-26	18-Aug-26	22-Jul-26A	26-Jul-26A	$80,437.50	$80,437.50	$80,437.50	26.00
MLTX02-004CN-108	AAC Panels Works for Walls	1200	100%	100%	15-Jul-26	28-Jul-26	22-Jul-26A	23-Jul-26A	$48,262.50	$48,262.50	$48,262.50	10.00
MLTX02-004CN-108	Parpet Works and Lintels	8.00	100%	100%	10-Aug-26	18-Aug-26	26-Jul-26A	26-Jul-26A	$16,087.50	$16,087.50	$16,087.50	7.00
MLTX02-004CN-108	AAC Panels Works for Slabs	1000	100%	100%	29-Jul-26	09-Aug-26	23-Jul-26A	26-Jul-26A	$16,087.50	$16,087.50	$16,087.50	7.00
UNDER GROUNDSEPTIC TANK		1810	100%	100%	06-Jun-26	27-Jun-26	06-Jun-26A	27-Jun-26A	$33,930.00	$33,930.00	$33,930.00	0.00
MLTX02-004CN-10860	Plain Concrete Under Footing	4.00	100%	100%	06-Jun-26	10-Jun-26	06-Jun-26A	10-Jun-26A	$1,170.00	$1,170.00	$1,170.00	0.00
MLTX02-004CN-10890	ReinforcedConcrete Works for Tank SlabIncludingShutteing and Steel Fixing	4.60	100%	100%	22-Jun-26	27-Jun-26	22-Jun-26A	27-Jun-26A	$8,775.00	$8,775.00	$8,775.00	0.00
MLTX02-004CN-10870	ReinforcedConcrete Works for Tank FoundationIncludingShutteing and Steel Fixing	8.60	100%	100%	10-Jun-26	20-Jun-26	10-Jun-26A	20-Jun-26A	$7,605.00	$7,605.00	$7,605.00	0.00
MLTX02-004CN-10880	ReinforcedConcrete Works for Tank Walls including Steel Fixing	3.80	100%	100%	17-Jun-26	21-Jun-26	17-Jun-26A	21-Jun-26A	$16,380.00	$16,380.00	$16,380.00	0.00
THERMAL& MOISTERPROTECTION		4684	100%	100%	06-Jun-26	18-Jul-26	06-Jun-26A	22-Jul-26A	$10,090.16	$10,090.16	$10,309.16	-330
ANTITERMITCONTROL		2024	100%	100%	06-Jun-26	29-Jun-26	06-Jun-26A	29-Jun-26A	$4,387.50	$4,387.50	$4,387.50	0.00
MLTX02-004CN-105	AntiTermite Works Under Foundation	7.38	100%	100%	06-Jun-26	14-Jun-26	06-Jun-26A	14-Jun-26A	$1,755.00	$1,755.00	$1,755.00	0.00
MLTX02-004CN-105	AntiTermite Works Under Slab onGradeand Gratle Beams	5.40	100%	100%	23-Jun-26	29-Jun-26	23-Jun-26A	29-Jun-26A	$2,632.50	$2,632.50	$2,632.50	0.00
POLYETHYLENESHEET		2064	100%	100%	06-Jun-26	29-Jun-26	06-Jun-26A	29-Jun-26A	$2,193.75	$2,193.75	$2,193.75	0.00
MLTX02-004CN-105	Water ProofingUnderBlinding Concrete(PolythelenSheet)	7.38	100%	100%	06-Jun-26	14-Jun-26	06-Jun-26A	14-Jun-26A	$87.50	$87.50	$87.50	0.00
MLTX02-004CN-105	Water ProofingUnderSlab on Grade (Polythelen Sheet)	5.80	100%	100%	23-Jun-26	29-Jun-26	23-Jun-26A	29-Jun-26A	$1,316.25	$1,316.25	$1,316.25	0.00
EPOXY		1300	100%	100%	05-Jul-26	18-Jul-26	14-Jul-26A	22-Jul-26A	$3,727.91	$3,727.91	$3,727.91	4.70
MLTX02-004CN-111	Surface Preparation for Epoxy Coating	5.00	100%	100%	05-Jul-26	09-Jul-26	14-Jul-26A	21-Jul-26A	$1,168.54	$1,168.54	$1,168.54	-150
MLTX02-004CN-111	EpoxyCoating forWalls andSlabof Tank	7.00	100%	100%	11-Jul-26	18-Jul-26	21-Jul-26A	22-Jul-26A	$2,559.38	$2,559.38	$2,559.38	5.70
MASONARY WORK		5.00	100%	100%	09-Jul-26	14-Jul-26	26-Jul-26A	28-Jul-26A	$12,285.00	$12,285.00	$12,285.00	2.00
MLTX02-004CN-11 090	CMU MasonaryWorksIncluding all Accessories	5.00	100%	100%	09-Jul-26	14-Jul-26	26-Jul-26A	28-Jul-26A	$12,285.00	$12,285.00	$12,285.00	2.00
THERMAL& MOISTER PROTECTION		2200	100%	100%	23-Aug-26	15-Sep-26	26-Sep-26 A	19-Oct-26A	$34,470.25	$34,470.25	$34,700.25	0.00
MLTX02-004CN-11 050	PreparingSurface andPreliminaryWorksforToilets Waterpoofing	2.00	100%	100%	23-Aug-26	24-Aug-26	15-Oct-26A	19-Oct-26A	$2,106.00	$2,106.00	$2,106.00	-200
MLTX02-004CN-11 070	FinalizeWaterProofing Worksfor Toilets	6.00	100%	100%	25-Aug-26	31-Aug-26	06-Oct-26A	10-Oct-26A	$4,914.00	$4,914.00	$4,914.00	2.00
MLTX02-004CN-11 060	PreparingSurface andPreliminaryWorksforRoofing andWet Areas Insulation	5.00	100%	100%	01-Sep-26	06-Sep-26	26-Sep-26 A	26-Sep-26A	$11,072.10	$11,072.10	$11,072.10	4.00
MLTX02-004CN-11 080	FinalizeWaterProofing Worksfor Roofingand Wet Areas	8.00	100%	100%	07-Sep-26	15-Sep-26	27-Sep-26 A	17-Oct-26A	$16,608.15	$16,608.15	$16,608.15	-1000
MECHANICALWORK		9200	100%	2725%	01-Sep-26	20-Oct-26	06-Jul-26A	21-Dec-26	$8,847.53	$104,832.00	$3,917.55.88	- 104.00
HVAC SYSTEM		7500	100%	3357%	15-Sep-26	20-Oct-26	10-Aug-26 A	21-Dec-26	$2,188.50	$9360.00	$27885.00	-8400
MLTX02-004CN-11500	Installand FinishHVAC and VentilationWorksIncludingSplitAir Units	6.00	100%	0%	14-Oct-26	20-Oct-26	15-Dec-26	21-Dec-26	$1,462.50	$000	$14625.00	0.00
MLTX02-004CN-11490	Exhaust, Air Ducts Installationwithall Accessories	8.00	100%	0%	19-Sep-26	28-Sep-26	27-Oct-26	04-Nov-26	$3,900.00	$000	$3,900.00	0.00
MLTX02-004CN-11480	Preliminay HVAC and Ventilation Works	3.00	100%	100%	15-Sep-26	17-Sep-26	10-Aug-26 A	10-Aug-26A	$9,360.00	$9360.00	$9,360.00	2.00
WATERSUPPLYSYSTEM		8100	100%	3.26%	03-Sep-26	10-Oct-26	06-Jul-26A	10-Dec-26	$2,124.27.50	$6922.50	$2,124.27.50	- 106.00
MLTX02-004CN-11530	Installing ofHDPE Pipes andValvesforWaterSupplyNetwok	3.00	100%	0%	09-Sep-26	12-Sep-26	29-Oct-26	01-Nov-26	$3,900.00	$000	$39000.00	0.00
MLTX02-004CN-11550	Installing ofBooster PumpUnitsIncluding fittings and accessories	7.00	100%	0%	29-Sep-26	06-Oct-26	08-Nov-26	15-Nov-26	$5,100.00	$000	$51000.00	0.00
MLTX02-004CN-11560	Installing ofGRP Tanks	8.00	100%	0%	19-Sep-26	28-Sep-26	29-Oct-26	07-Nov-26	$1,040.00.00	$000	$1,040.00.00	0.00
MLTX02-004CN-11520	Installing ofValvesand fittings	2.00	100%	0%	07-Sep-26	08-Sep-26	27-Oct-26	28-Oct-26	$975.00	$000	$9,750.00	0.00
MLTX02-004CN-11860	Installing ofWater Heater	4.00	100%	0%	06-Oct-26	10-Oct-26	07-Dec-26	10-Dec-26	$1,755.00	$000	$1,755.00	0.00
MLTX02-004CN-11540	Installing ofPPR Pipes andFittings for WaterNetwork	3.00	100%	100%	03-Sep-26	06-Sep-26	04-Jul-26A	09-Aug-26A	$6,922.50	$6922.50	$6,922.50	-2855
SEWERDRAIN AGESYSTEM		8800	100%	6214%	01-Sep-26	15-Oct-26	04-Jul-26A	16-Dec-26	$1,424.91.38	$8,859.95	$1,424.91.38	- 104.00
MLTX02-004CN-11600	Installing ofPlumping Fixturesand Accessories	2.00	100%	0%	19-Sep-26	20-Sep-26	21-Nov-26	22-Nov-26	$1,025.93.38	$000	$10359.38	0.00
MLTX02-004CN-11850	Installing Inspection Chamber forSewageNetwok	9.00	100%	0%	03-Sep-26	13-Sep-26	27-Oct-26	05-Nov-26	$12,187.50	$000	$12187.50	0.00
MLTX02-004CN-11870	Installing ofToilet Fixturesand Accessoires Such as Cbsetsand Basins	9.00	100%	0%	06-Oct-26	15-Oct-26	07-Dec-26	16-Dec-26	$3,139.50	$000	$31395.00	0.00
MLTX02-004CN-11590	Installing UPVC Pipes for Sewage Network	2.00	100%	100%	01-Sep-26	02-Sep-26	04-Jul-26A	09-Aug-26A	$1,176.82.5	$1,176.82.5	$11768.25	-2960
MLTX02-004CN-11580	Installing UPVC Pipes for External Connecton for Sewage Network	4.00	100%	100%	14-Sep-26	17-Sep-26	08-Oct-26A	10-Oct-26A	$7,678.1.25	$7,678.1.25	$76781.25	2.00
FIREPROTECTION		4.00	100%	0%	17-Oct-26	20-Oct-26	17-Dec-26	21-Dec-26	$1,950.00	$000	$1,950.00	0.00
MLTX02-004CN-11620	Installing ofFireFighting Extinguisherand accessories (PIE-1, PIE-2)	4.00	100%	0%	17-Oct-26	20-Oct-26	17-Dec-26	21-Dec-26	$1,950.00	$000	$1,950.00	0.00
ELECTRICALWORKS		12600	100%	3954%	19-Aug-26	25-Oct-26	30-Jul-26A	26-Dec-26	$3,765.26.25	$148882.50	$3,765.26.25	-7000
ROUGH-N WORKS		3600	100%	100%	19-Aug-26	30-Aug-26	30-Jul-26A	26-Aug-26A	$1,488.82.50	$148882.50	$1,488.82.50	-1400
MLTX02-004CN-11660	Preliminay Woks forPanelBoards	1000	100%	100%	19-Aug-26	30-Aug-26	11-Aug-26 A	26-Aug-26A	$7,605.00	$7,605.00	$76050.00	-400
MLTX02-004CN-11670	Preliminay Woks forCableWorks	1000	100%	100%	19-Aug-26	30-Aug-26	11-Aug-26 A	26-Aug-26A	$1,070.00.04	$1,070.00.04	$10700.04	-400
MLTX02-004CN-11680	Preliminay Woks forSockets andPowerPoints	1000	100%	100%	19-Aug-26	30-Aug-26	30-Jul-26A	30-Jul-26A	$9,230.91	$9230.91	$9,230.91	9.00
MLTX02-004CN-11690	Preliminay Woks forLightningWorks	1000	100%	100%	19-Aug-26	30-Aug-26	11-Aug-26 A	26-Aug-26A	$9,750.00	$9750.00	$9,750.00	-400
MLTX02-004CN-11700	Preliminay Woks forData& TelecommunicationSystem	1000	100%	100%	19-Aug-26	30-Aug-26	11-Aug-26 A	26-Aug-26A	$12,285.00	$12,285.00	$12285.00	-400
MLTX02-004CN-11720	Preliminay Woks forSecurity and Access Contol System	1000	100%	100%	19-Aug-26	30-Aug-26	11-Aug-26 A	26-Aug-26A	$15,266.55	$15,266.55	$15266.55	-400
MLTX02-004CN-11650	Preliminay Woks forEarthing Works	1000	100%	100%	19-Aug-26	30-Aug-26	11-Aug-26 A	26-Aug-26A	$15,600.00	$15,600.00	$15600.00	-400
FIXTURE WORKS		1000	100%	0%	14-Oct-26	25-Oct-26	15-Dec-26	26-Dec-26	$2,276.43.75	$000	$2,276.43.75	0.00
MLTX02-004CN-11780	Installing ofFireautomationand Fire Alarm System	4.00	100%	0%	21-Oct-26	25-Oct-26	22-Dec-26	26-Dec-26	$3,432.00.00	$000	$34320.00	0.00
MLTX02-004CN-11740	Installing andFinish Woks ofPanelBoards	1000	100%	0%	14-Oct-26	25-Oct-26	15-Dec-26	26-Dec-26	$8,407.50.00	$000	$84075.00	0.00
MLTX02-004CN-11760	Installing andFinalize Worksof Sockets and PowerPoints	4.00	100%	0%	17-Oct-26	20-Oct-26	17-Dec-26	21-Dec-26	$1,384.63.7	$000	$13846.37	0.00
MLTX02-004CN-11790	Installing andFinalize Worksof Lighting Woks indudingLightFixtures	4.00	100%	0%	17-Oct-26	20-Oct-26	17-Dec-26	21-Dec-26	$1,605.00.06	$000	$16050.00	0.00
MLTX02-004CN-11750	Installing Data andTelecommunicaton System with allAccessories	4.00	100%	0%	17-Oct-26	20-Oct-26	17-Dec-26	21-Dec-26	$1,842.75.00	$000	$18427.50	0.00
MLTX02-004CN-11830	Installing andFinalize Worksof Seauityand Access ControlSystem	6.00	100%	0%	14-Oct-26	20-Oct-26	15-Dec-26	21-Dec-26	$2,289.99.38	$000	$22899.38	0.00
MLTX02-004CN-11770	Installing andFinalize Worksof EathingWorks	6.00	100%	0%	14-Oct-26	20-Oct-26	15-Dec-26	21-Dec-26	$2,340.00.00	$000	$23400.00	0.00
MLTX02-004CN-11820	Installing andFinalize Worksof Lightning Protection System	6.00	100%	0%	14-Oct-26	20-Oct-26	15-Dec-26	21-Dec-26	$1,462.50.00	$000	$14625.00	0.00
DOORS/WINDOWS		5900	5592%	0%	19-Aug-26	02-Nov-26	27-Oct-26	03-Jan-27	$3,916.4.25	$000	$68250.00	5.00
MLTX02-004CN-11 110	Preliminay Woks ForDoors	3.00	100%	0%	19-Aug-26	22-Aug-26	27-Oct-26	29-Oct-26	$3,900.00	$000	$3,900.00	0.00
MLTX02-004CN-11 120	FinalizeMetalDoorsfor Toilets Building	7.00	100%	0%	18-Oct-26	25-Oct-26	15-Dec-26	22-Dec-26	$5,850.00	$000	$5,850.00	0.00
MLTX02-004CN-11 130	FinalizeGlazzedCurtain Wall Works	7.00	1429%	0%	26-Oct-26	02-Nov-26	27-Dec-26	03-Jan-27	$5,014.2.9	$000	$35100.00	0.00
MLTX02-004CN-11 100	Preliminay Woks ForWindows/CurtainWall	2.00	100%	0%	19-Aug-26	20-Aug-26	07-Nov-26	08-Nov-26	$2,340.00.00	$000	$23400.00	0.00
METALWORKS		2944	100%	7143%	19-Jul-26	17-Oct-26	20-Sep-26 A	07-Nov-26	$1,365.0.00	$9750.00	$13650.00	36.48

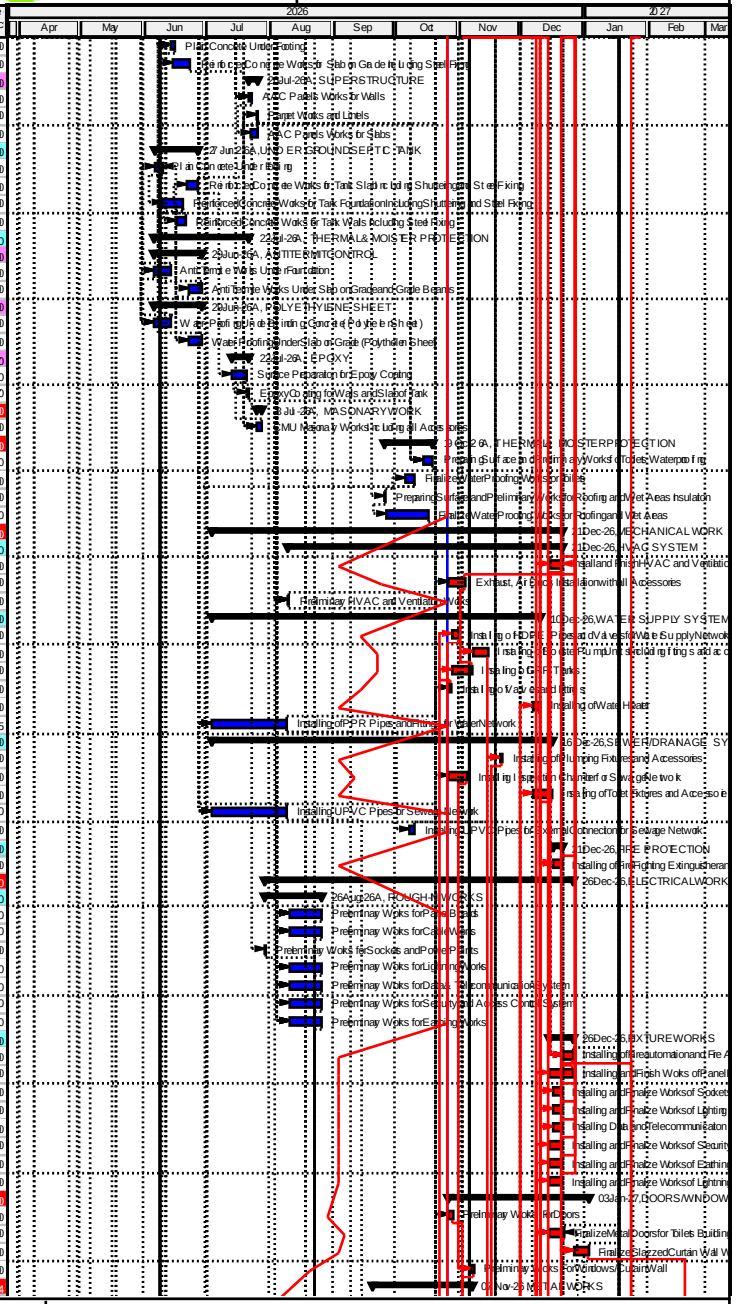

© Oracle Corporation

ActivityID	ActivityName	Orginal Duration	Schedule %	Performance% Complete	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Variance - BL Project
MLTX02-004CN-11150	Installationof DICoverfor Tank	1000	100%	0%	19 Jul-26	29Jul-26	27 Oct2 6	07Nov-26	$3 900.00	$000	$3 900.00	0.00
MLTX02-004CN-11160	Installationof GalvanizedSteelLadder	1200	100%	100%	19 Sep-26	03Oct-26	21 Sep 26 A	03Oct-26A	$5 850.00	$5850.00	$5 850.00	2.44
MLTX02-004CN-11170	Installationof GalvanizedSteelRoofScupper	1200	100%	100%	04 Oct 2 6	17Oct-26	20 Sep 26 A	20Sep-26A	$3 900.00	$3900.00	$3 900.00	12.00
FINISHING WORKS		7456	100%	344%	01 Sep-26	17Oct-26	29 Aug 26 A	17Dec-26	$1 445 14.50	$4 971 8.50	$1 445 11.50	-5556
FLOORFINISHES		3400	100%	0%	07 Sep-26	17Oct-26	09 Nov 26	17Dec-26	$1 716 0.00	$000	$17160.00	0.00
MLTX02-004CN-11200	Ceramic Tiles FloorFinishWorks	2.00	100%	0%	07 Sep-26	08Sep-26	09 Nov 26	10Nov-26	$1 189 5.00	$000	$11895.00	0.00
MLTX02-004CN-11210	Granite TilesFloorFinish Works	4.00	100%	0%	09 Sep-26	13Sep-26	11 Nov 26	15Nov-26	$2 925.00	$000	$2 925.00	0.00
MLTX02-004CN-11220	EpoxyCoaton Concrete floor	3.00	100%	0%	14 Oct 2 6	17Oct-26	15 Dec 26	17Dec-26	$1 170.00	$000	$1 170.00	0.00
MLTX02-004CN-11230	Ceramic SkirtingTiles Finish Works	4.00	100%	0%	14 Sep-26	17Sep-26	16 Nov 26	19Nov-26	$1 170.00	$000	$1 170.00	0.00
WALLFINISHES		7356	100%	4355%	01 Sep-26	15Oct-26	29 Aug 26 A	16Dec-26	$1 141 72.50	$4 971 8.50	$1 141 12.50	-5556
MLTX02-004CN-11300	PaintingFinishWorks forExtenal Walls	7.00	100%	0%	13 Sep-26	20Sep-26	02 Nov 26	09Nov-26	$1 047 8.00	$000	$10478.00	0.00
MLTX02-004CN-11320	Phendic Patitons for Toilets	7.00	100%	0%	28 Sep-26	05Oct-26	29 Nov 26	06Dec-26	$3 120 0.00	$000	$31200.00	0.00
MLTX02-004CN-11260	Glass Partitions includingallaccessoiesand doors	7.00	100%	0%	06 Oct 2 6	13Oct-26	07 Dec 26	14Dec-26	$1 228 5.00	$000	$12285.00	0.00
MLTX02-004CN-11270	Granite Cappingfor Parpet	2.00	100%	0%	16 Sep-26	17Sep-26	27 Oct2 6	28Oct-26	$8 15.00	$000	$8 151.00	0.00
MLTX02-004CN-11840	PaintingFinishWorks forIntenalWalls	2.00	100%	0%	14 Oct 2 6	15Oct-26	15 Dec 26	16Dec-26	$2 340.00	$000	$2 340.00	0.00
MLTX02-004CN-11280	Prelminay Woks for Wall Finish Worksincluding Plastering (Intenal)	5.00	100%	100%	01 Sep-26	06Sep-26	29 Aug 26 A	09Sep-26A	$1 836 9.00	$1 836 9.00	$18369.00	-556
MLTX02-004CN-11290	Prelminay Woks for Wall Finish Works(Extenal)	1000	100%	100%	01 Sep-26	12Sep-26	10 Sep 26 A	12Sep-26A	$6 552.00	$6552.00	$6 552.00	8.44
MLTX02-004CN-11310	Ceramic Finish Worksfor Walls	5.00	100%	100%	09 Sep-26	14Sep-26	12 Sep 26 A	14Sep-26A	$1 559 7.50	$1 559 7.50	$15597.50	2.00
MLTX02-004CN-11250	Store Cladding FinishWorksforExtemal Walls	5.00	100%	100%	21 Sep-26	27Sep-26	19 Sep 26 A	26Sep-26A	$9 100.00	$9100.00	$9 100.00	-100
CELLING FINISHES		1000	100%	0%	07 Sep-26	30Sep-26	27 Oct2 6	07Nov-26	$1 318 2.00	$000	$13182.00	10.00
MLTX02-004CN-11350	PaintingFinishWorks forCeiling	3.00	100%	0%	28 Sep-26	30Sep-26	04 Nov 26	07Nov-26	$1 638 0.00	$000	$1 638 0.00	0.00
MLTX02-004CN-11360	Gypsum BoardSuspended Ceiling finishWorksForCeiling	7.00	100%	0%	19 Sep-26	27Sep-26	27 Oct2 6	03Nov-26	$6 926.40	$000	$6 926.40	0.00
MLTX02-004CN-11340	Prelminay Woks for Ceiling Painting Woks	3.00	100%	0%	07 Sep-26	09Sep-26	27 Oct2 6	29Oct-26	$4 617.60	$000	$4 617.60	0.00
SPECIALTIES WORK		1500	100%	0%	21 Sep-26	08Oct-26	23 Nov 26	09Dec-26	$3 900.00	$000	$39000.00	0.00
MLTX02-004CN-11390	SantaryFixtures andAccessoiesWorks	5.00	100%	0%	21 Sep-26	27Sep-26	23 Nov 26	28Nov-26	$1 462 5.00	$000	$14625.00	0.00
MLTX02-004CN-11380	Installationof PhenolicLocker	3.00	100%	0%	06 Oct 2 6	08Oct-26	07 Dec 26	09Dec-26	$2 437 5.00	$000	$24375.00	0.00
TESTING & COMMISSIONING		6400	0%	0%	05 Nov-26	12Jan-27	30 Jan 2 7	18Apr-27	$000	$000	$0.00	-500
MLTX02-0047C-11860	Testing and Commissioning forMEP Woks for PlaygroundArea	1000	0%	0%	02 Jan 2 7	12Jan-27	07 Apr2 7	18Apr-27	$000	$000	$0.00	0.00
MLTX02-0047C-11870	Testing and Commissioning forMEP Woks for ToletServiceBuilding	2200	0%	0%	05 Nov-26	30Nov-26	30 Jan 2 7	24Feb-27	$000	$000	$0.00	0.00
MLTX02-0047C-11880	Testing and Commissioning forMEP Woks for LantscapeWorks	2200	0%	0%	01 Dec-26	26Dec-26	25 Feb 2 7	25Mar-27	$000	$000	$0.00	0.00
JAZAN		34900	3923%	2889%	26 Mar2 6	25Jan-27	26 Mar2 6A	19May-27	$4190.2717 4	$3085.78928	$10680.071.52	-9100
MOBILIZATION		6300	0%	0%	26 Mar2 6	10Jun-26	26 Mar2 6A	10Jun-26A	$000	$000	$0.00	0.00
TOPOGRAPHICSURVEY		400	0%	0%	26 Mar2 6	30Mar-26	26 Mar2 6A	30Mar-26A	$000	$000	$0.00	0.00
MLTX02-004MB-1860	Site Survey Woks	4.00	100%	100%	26 Mar2 6	30Mar-26	26 Mar2 6A	30Mar-26A	$000	$000	$0.00	0.00
SITEFACILITES & OFFICES		5575	0%	0%	26 Mar2 6	02Jun-26	26 Mar2 6A	02Jun-26A	$000	$000	$0.00	0.00
MLTX02-004MB-1740	Manpower Mobalizaton	3150	100%	100%	16 Apr2 6	23May-26	16 Apr2 6A	23May-26A	$000	$000	$0.00	0.00
MLTX02-004MB-1750	Equipment Mobalization	2.00	100%	100%	06 May-26	07May-26	06 May 26 A	07May-26A	$000	$000	$0.00	0.00
MLTX02-004MB-1770	Site Layout Plan	4.00	100%	100%	26 Mar2 6	30Mar-26	26 Mar2 6A	30Mar-26A	$000	$000	$0.00	0.00
MLTX02-004MB-1780	Clear & Grub forOffices & AccessRoad	3.00	100%	100%	31 Mar2 6	02Apr-26	31 Mar2 6A	02Apr-26A	$000	$000	$0.00	0.00
MLTX02-004MB-1790	ConstuctSiteAccess Roads	4.00	100%	100%	31 Mar2 6	04Apr-26	31 Mar2 6A	04Apr-26A	$000	$000	$0.00	0.00
MLTX02-004MB-1800	ConstuctTemporay Fence	3875	100%	100%	15 Apr2 6	02Jun-26	15 Apr2 6A	02Jun-26A	$000	$000	$0.00	0.00
MLTX02-004MB-1810	ConstuctSiteOffices & Storage	2.00	100%	100%	06 May-26	07May-26	06 May 26 A	07May-26A	$000	$000	$0.00	0.00
MLTX02-004MB-1820	InstallProject Signs	1800	100%	100%	20 Apr2 6	10May-26	20 Apr2 6A	10May-26A	$000	$000	$0.00	0.00
MLTX02-004MB-1830	InstallSiteFacilities	1.00	100%	100%	06 May-26	07May-26	06 May 26 A	07May-26A	$000	$000	$0.00	0.00
MLTX02-004MB-1840	Electrical Woks & Connections	1.00	100%	100%	06 May-26	07May-26	06 May 26 A	07May-26A	$000	$000	$0.00	0.00
MLTX02-004MB-1850	ConstuctParking Sheds	1.00	100%	100%	06 May-26	07May-26	06 May 26 A	07May-26A	$000	$000	$0.00	0.00
PRELIMINARY SUBMITTALS		5900	0%	0%	31 Mar2 6	10Jun-26	31 Mar2 6A	10Jun-26A	$000	$000	$0.00	0.00
PREPARATIONS& SUBMITTALBY CONTRACTORS		2700	0%	0%	31 Mar2 6	30Apr-26	31 Mar2 6A	30Apr-26A	$000	$000	$0.00	0.00
MLTX02-004MB-1760	Preparation andSubmittal ofDetaledWorkOrderProgramme(Baseline)	2500	100%	100%	31 Mar2 6	28Apr-26	31 Mar2 6A	28Apr-26A	$000	$000	$0.00	0.00
MLTX02-004MB-1870	Preparation andSubmittal ofProject Execution Plan	2700	100%	100%	31 Mar2 6	30Apr-26	31 Mar2 6A	30Apr-26A	$000	$000	$0.00	0.00
MLTX02-004MB-1880	Submissionof Contactor Project Quality Plan	1000	100%	100%	31 Mar2 6	11Apr-26	31 Mar2 6A	11Apr-26A	$000	$000	$0.00	0.00
MLTX02-004MB-1890	Submissionof Construction Safety& EnvironmentalManagement Plan	1000	100%	100%	31 Mar2 6	11Apr-26	31 Mar2 6A	11Apr-26A	$000	$000	$0.00	0.00
MLTX02-004MB-1900	Preparation andSubmittal ofOrganization Chat	8.00	100%	100%	31 Mar2 6	08Apr-26	31 Mar2 6A	08Apr-26A	$000	$000	$0.00	0.00
MLTX02-004MB-1910	Preparation andSubmittal ofCommunication Plan	8.00	100%	100%	31 Mar2 6	08Apr-26	31 Mar2 6A	08Apr-26A	$000	$000	$0.00	0.00
APPROVALS BYEMPLOYERS		5100	0%	0%	09 Apr2 6	10Jun-26	09 Apr2 6A	10Jun-26A	$000	$000	$0.00	0.00
MLTX02-004MB-1920	Appoval of DetailedWorkOrderProgramme (Baseline)	1.00	100%	100%	29 Apr2 6	29Apr-26	29 Apr2 6A	29Apr-26A	$000	$000	$0.00	0.00
MLTX02-004MB-1930	Appoval of Project Execution Plan	1.00	100%	100%	13 May-26	13May-26	13 May 26 A	13May-26A	$000	$000	$0.00	0.00
MLTX02-004MB-1940	Appoval of ContactorProject QualityPlan	1900	100%	100%	09 Apr2 6	30Apr-26	09 Apr2 6A	30Apr-26A	$000	$000	$0.00	0.00
MLTX02-004MB-1950	Appoval of Constuction Safety & EnvironmentalManagement Plan	1.00	100%	100%	10 Jun 2 6	10Jun-26	10 Jun 2 6A	10Jun-26A	$000	$000	$0.00	0.00
MLTX02-004MB-1960	Appoval of Organization Chat	1000	100%	100%	09 Apr2 6	20Apr-26	09 Apr2 6A	20Apr-26A	$000	$000	$0.00	0.00
MLTX02-004MB-1970	Appoval of Communication Plan	1000	100%	100%	09 Apr2 6	20Apr-26	09 Apr2 6A	20Apr-26A	$000	$000	$0.00	0.00
ENGINEERING		19100	0%	0%	31 Mar2 6	02Aug-26	31 Mar2 6A	12Nov-26	$000	$000	$0.00	-8700
SHOP DRAWINGS		14400	0%	0%	31 Mar2 6	21Jul-26	31 Mar2 6A	26Aug-26A	$000	$000	$0.00	-3100
SHOP DRAWINGS SUBMISSDN		13400	0%	0%	31 Mar2 6	09Jul-26	31 Mar2 6A	25Aug-26A	$000	$000	$0.00	-4000
SHOP DRAWINGSUBMITTALS FOR EARTHINGWORKS		6800	0%	0%	31 Mar2 6	21Jun-26	31 Mar2 6A	21Jun-26A	$000	$000	$0.00	0.00
MLTX02-004EN-7830	ShopDWG SubmittalforLayoutPlan	1500	100%	100%	31 Mar2 6	16Apr-26	31 Mar2 6A	16Apr-26A	$000	$000	$0.00	0.00
MLTX02-004EN-7840	ShopDWG SubmittalforSetting Out	2100	100%	100%	31 Mar2 6	23Apr-26	31 Mar2 6A	25Apr-26A	$000	$000	$0.00	0.00
MLTX02-004EN-7850	ShopDWG SubmittalforGrading Layout Plan	600	100%	100%	31 Mar2 6	06Apr-26	31 Mar2 6A	06Apr-26A	$000	$000	$0.00	0.00
MLTX02-004EN-7860	ShopDWG SubmittalforCurb Setting OutPoints	1.00	100%	100%	23 May-26	23May-26	23 May 26 A	23May-26A	$000	$000	$0.00	0.00
MLTX02-004EN-7870	ShopDWG SubmittalforSigning & MakingLayoutPlan	1.00	100%	100%	21 Jun 2 6	21Jun-26	21 Jun 2 6A	21Jun-26A	$000	$000	$0.00	0.00
MLTX02-004EN-7880	ShopDWG SubmittalforStandards Details	1.00	100%	100%	21 May-26	21May-26	21 May 26 A	21May-26A	$000	$000	$0.00	0.00

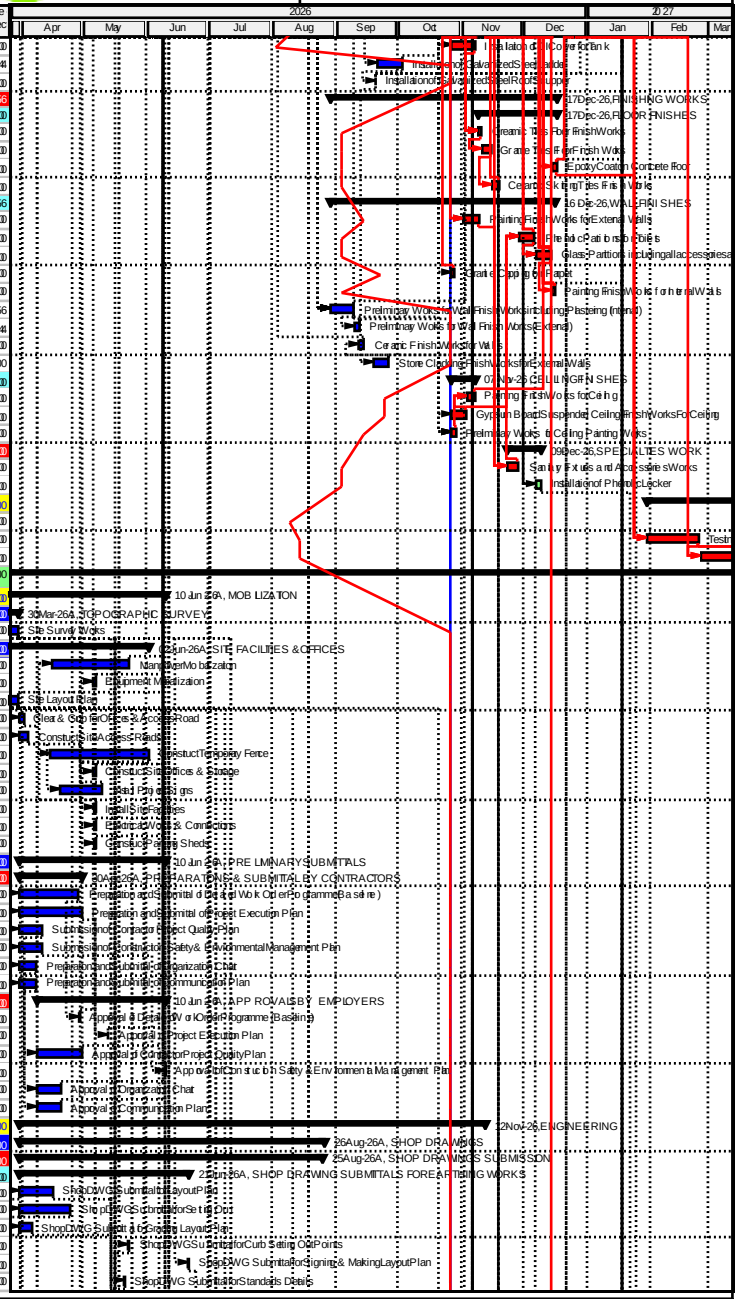


Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work

TASK filter: All Activities


© Oracle Corporation

ActivityID	ActivityName	Orginal Duration	Schedule %	Performance% Complete	BL Project Stat	BL Project Finish	Stat	Finish	Planned Value Cos	Earned Value Cos	Budgeted Tot Cos	Variance - BL Project
	SHOP DRAWIN GSUBMITTALS FOR SERVCE/TOILETWORKS	13400	0%	0%	31 Mar 2 6	09Jul-26	31 Mar2 6A	25Aug-26A	$000	$000	$0 00	-4000
	ARCHITECTURE WORKS	1200	0%	0%	31 Mar 2 6	13Apr-26	31 Mar2 6A	13Apr-26A	$000	$000	$0 00	0.00
MLTX02-004EN-821	ShopDWG SubmittalforFloorPlan	1200	100%	100%	31 Mar 2 6	13Apr-26	31 Mar2 6A	13Apr-26A	$000	$000	$0 00	0.00
MLTX02-004EN-822	ShopDWG SubmittalforElevations	1200	100%	100%	31 Mar 2 6	13Apr-26	31 Mar2 6A	13Apr-26A	$000	$000	$0 00	0.00
MLTX02-004EN-823	ShopDWG SubmittalforSections	1200	100%	100%	31 Mar 2 6	13Apr-26	31 Mar2 6A	13Apr-26A	$000	$000	$0 00	0.00
MLTX02-004EN-824	ShopDWG SubmittalforCeiling Plan	1200	100%	100%	31 Mar 2 6	13Apr-26	31 Mar2 6A	13Apr-26A	$000	$000	$0 00	0.00
MLTX02-004EN-825	ShopDWG SubmittalforFinishes Plan	1200	100%	100%	31 Mar 2 6	13Apr-26	31 Mar2 6A	13Apr-26A	$000	$000	$0 00	0.00
MLTX02-004EN-826	ShopDWG SubmittalforToilet Details	1200	100%	100%	31 Mar 2 6	13Apr-26	31 Mar2 6A	13Apr-26A	$000	$000	$0 00	0.00
MLTX02-004EN-827	ShopDWG SubmittalforDoorsWindows Schedule	1200	100%	100%	31 Mar 2 6	13Apr-26	31 Mar2 6A	13Apr-26A	$000	$000	$0 00	0.00
	STRUCTUREWORKS	2000	0%	0%	08 Apr2 6	30Apr-26	08 Apr2 6A	30Apr-26A	$000	$000	$0 00	0.00
MLTX02-004EN-828	ShopDWG SubmittalforFoundationPlan	2000	100%	100%	08 Apr2 6	30Apr-26	08 Apr2 6A	30Apr-26A	$000	$000	$0 00	0.00
MLTX02-004EN-829	ShopDWG SubmittalforGroundFloorFraming Plan	2000	100%	100%	08 Apr2 6	30Apr-26	08 Apr2 6A	30Apr-26A	$000	$000	$0 00	0.00
MLTX02-004EN-830	ShopDWG SubmittalforSections/Details	2000	100%	100%	08 Apr2 6	30Apr-26	08 Apr2 6A	30Apr-26A	$000	$000	$0 00	0.00
	MECHANCALWORKS	3800	0%	0%	08 Apr2 6	21May-26	08 Apr2 6A	21May-26A	$000	$000	$0 00	0.00
MLTX02-004EN-831	ShopDWG SubmittalforHVAC Plan	6.00	100%	100%	08 Apr2 6	14Apr-26	08 Apr2 6A	14Apr-26A	$000	$000	$0 00	0.00
MLTX02-004EN-832	ShopDWG SubmittalforExhaustAirPlan	6.00	100%	100%	08 Apr2 6	14Apr-26	08 Apr2 6A	14Apr-26A	$000	$000	$0 00	0.00
MLTX02-004EN-833	ShopDWG SubmittalforHVAC Equipment Schedule	6.00	100%	100%	08 Apr2 6	14Apr-26	08 Apr2 6A	14Apr-26A	$000	$000	$0 00	0.00
MLTX02-004EN-834	ShopDWG SubmittalforFireFighting Layout	6.00	100%	100%	08 Apr2 6	14Apr-26	08 Apr2 6A	14Apr-26A	$000	$000	$0 00	0.00
MLTX02-004EN-835	ShopDWG SubmittalforWaterSupply Layout	1.00	100%	100%	06 May-26	06May-26	06 May 25 A	06May-26A	$000	$000	$0 00	0.00
MLTX02-004EN-836	ShopDWG SubmittalforWaterSupply Details	6.00	100%	100%	08 Apr2 6	14Apr-26	08 Apr2 6A	14Apr-26A	$000	$000	$0 00	0.00
MLTX02-004EN-837	ShopDWG SubmittalforDrainage Layout	1.00	100%	100%	21 May-26	21May-26	21 May 25 A	21May-26A	$000	$000	$0 00	0.00
MLTX02-004EN-838	ShopDWG SubmittalforDrainage Details	6.00	100%	100%	08 Apr2 6	14Apr-26	08 Apr2 6A	14Apr-26A	$000	$000	$0 00	0.00
MLTX02-004EN-892	ShopDWG SubmittalforDut RoutingLayout	6.00	100%	100%	08 Apr2 6	14Apr-26	08 Apr2 6A	14Apr-26A	$000	$000	$0 00	0.00
MLTX02-004EN-893	ShopDWG SubmittalforDiffusersLayout	1.00	100%	100%	21 May-26	21May-26	21 May 25 A	21May-26A	$000	$000	$0 00	0.00
	ELECTRCALWORKS	12700	0%	0%	08 Apr2 6	09Jul-26	08 Apr2 6A	25Aug-26A	$000	$000	$0 00	-4000
MLTX02-004EN-839	ShopDWG SubmittalforLighting layout	1000	100%	100%	08 Apr2 6	19Apr-26	08 Apr2 6A	19Apr-26A	$000	$000	$0 00	0.00
MLTX02-004EN-840	ShopDWG SubmittalforPower layout	2.00	100%	100%	06 May-26	07May-26	06 May 25 A	07May-26A	$000	$000	$0 00	0.00
MLTX02-004EN-841	ShopDWG SubmittalforPower SingleLineDiagram	2.00	100%	100%	06 May-26	07May-26	06 May 25 A	07May-26A	$000	$000	$0 00	0.00
MLTX02-004EN-842	ShopDWG SubmittalforPanelBoardSchedules	2.00	100%	100%	06 May-26	07May-26	06 May 25 A	07May-26A	$000	$000	$0 00	0.00
MLTX02-004EN-843	ShopDWG SubmittalforLighting Installation Details	1000	100%	100%	08 Apr2 6	19Apr-26	08 Apr2 6A	19Apr-26A	$000	$000	$0 00	0.00
MLTX02-004EN-844	ShopDWG SubmittalforPower Installation Details	1000	100%	100%	08 Apr2 6	19Apr-26	08 Apr2 6A	19Apr-26A	$000	$000	$0 00	0.00
MLTX02-004EN-845	ShopDWG SubmittalforCableTrayInstallation Details	2.00	100%	100%	06 May-26	07May-26	06 May 25 A	07May-26A	$000	$000	$0 00	0.00
MLTX02-004EN-846	ShopDWG SubmittalforManhole& Ductbank Details	2.00	100%	100%	06 May-26	07May-26	06 May 25 A	07May-26A	$000	$000	$0 00	0.00
MLTX02-004EN-847	ShopDWG SubmittalforGrounding Details	2.00	100%	100%	06 May-26	07May-26	06 May 25 A	07May-26A	$000	$000	$0 00	0.00
MLTX02-004EN-848	ShopDWG SubmittalforLightningProtecton Details	1000	100%	100%	08 Apr2 6	19Apr-26	08 Apr2 6A	19Apr-26A	$000	$000	$0 00	0.00
MLTX02-004EN-849	ShopDWG SubmittalforFireAlarmInstallation Details	1100	100%	100%	08 Apr2 6	20Apr-26	08 Apr2 6A	20Apr-26A	$000	$000	$0 00	0.00
MLTX02-004EN-850	ShopDWG SubmittalforCCTV Details	5.00	100%	100%	05 Jul- 25	09Jul-26	25 Aug 25 A	25Aug-26A	$000	$000	$0 00	4.00
MLTX02-004EN-851	ShopDWG SubmittalforGrounding Layout	2.00	100%	100%	06 May-26	07May-26	06 May 25 A	07May-26A	$000	$000	$0 00	0.00
MLTX02-004EN-852	ShopDWG SubmittalforLightningProtecton System Layout	1000	100%	100%	08 Apr2 6	19Apr-26	08 Apr2 6A	19Apr-26A	$000	$000	$0 00	0.00
MLTX02-004EN-853	ShopDWG SubmittalforFireAlarmLayout	1100	100%	100%	08 Apr2 6	20Apr-26	08 Apr2 6A	20Apr-26A	$000	$000	$0 00	0.00
MLTX02-004EN-854	ShopDWG SubmittalforFireAlarmRiserDiagram	1100	100%	100%	08 Apr2 6	20Apr-26	08 Apr2 6A	20Apr-26A	$000	$000	$0 00	0.00
MLTX02-004EN-855	ShopDWG SubmittalforCCTV Layout	5.00	100%	100%	05 Jul- 25	09Jul-26	25 Aug 25 A	25Aug-26A	$000	$000	$0 00	4.00
MLTX02-004EN-856	ShopDWG SubmittalforCCTV Riser Diagram	5.00	100%	100%	05 Jul- 25	09Jul-26	25 Aug 25 A	25Aug-26A	$000	$000	$0 00	4.00
MLTX02-004EN-857	ShopDWG SubmittalforTelephone & Data Layout	1100	100%	100%	08 Apr2 6	20Apr-26	08 Apr2 6A	20Apr-26A	$000	$000	$0 00	0.00
MLTX02-004EN-858	ShopDWG SubmittalforTelephone & Data Riser Diagram	1100	100%	100%	08 Apr2 6	20Apr-26	08 Apr2 6A	20Apr-26A	$000	$000	$0 00	0.00
	SHOP DRAWIN GSSUBMITTALS FOR PLAYGROUND WORKS	13400	0%	0%	31 Mar 2 6	09Jul-26	31 Mar2 6A	25Aug-26A	$000	$000	$0 00	-4000
	ARCHITECTURE WORKS	3900	0%	0%	31 Mar 2 6	14May-26	31 Mar2 6A	14May-26A	$000	$000	$0 00	0.00
MLTX02-004EN-878	ShopDWG SubmittalforPlaygound Plan/Layout	1600	100%	100%	31 Mar 2 6	18Apr-26	31 Mar2 6A	18Apr-26A	$000	$000	$0 00	0.00
MLTX02-004EN-879	ShopDWG SubmittalforFumiture& Marking	2.00	100%	100%	13 May-26	14May-26	13 May 25 A	14May-26A	$000	$000	$0 00	0.00
MLTX02-004EN-880	ShopDWG SubmittalforSections	1600	100%	100%	31 Mar 2 6	18Apr-26	31 Mar2 6A	18Apr-26A	$000	$000	$0 00	0.00
MLTX02-004EN-881	ShopDWG SubmittalforInterlockPatten Plan	7.00	100%	100%	31 Mar 2 6	07Apr-26	31 Mar2 6A	07Apr-26A	$000	$000	$0 00	0.00
MLTX02-004EN-882	ShopDWG SubmittalforDoorsWindows Schedule	2.00	100%	100%	13 May-26	14May-26	13 May 25 A	14May-26A	$000	$000	$0 00	0.00
MLTX02-004EN-883	ShopDWG SubmittalforDome Internal Layout	2.00	100%	100%	13 May-26	14May-26	13 May 25 A	14May-26A	$000	$000	$0 00	0.00
	STRUCTUREWORKS	2.00	0%	0%	13 May-26	14May-26	13 May 25 A	14May-26A	$000	$000	$0 00	0.00
MLTX02-004EN-884	ShopDWG SubmittalforAir Dome System	2.00	100%	100%	13 May-26	14May-26	13 May 25 A	14May-26A	$000	$000	$0 00	0.00
MLTX02-004EN-885	ShopDWG SubmittalforFoundationof AirDome	2.00	100%	100%	13 May-26	14May-26	13 May 25 A	14May-26A	$000	$000	$0 00	0.00
MLTX02-004EN-886	ShopDWG SubmittalforAnchorBoltLayoutof Air Dome	2.00	100%	100%	13 May-26	14May-26	13 May 25 A	14May-26A	$000	$000	$0 00	0.00
	AIRDOMESYS TEM	2.00	0%	0%	13 May-26	14May-26	13 May 25 A	14May-26A	$000	$000	$0 00	0.00
MLTX02-004EN-887	ShopDWG SubmittalforAir Dome Structural Layout	2.00	100%	100%	13 May-26	14May-26	13 May 25 A	14May-26A	$000	$000	$0 00	0.00
MLTX02-004EN-888	ShopDWG SubmittalforMembrane PanelLayout	2.00	100%	100%	13 May-26	14May-26	13 May 25 A	14May-26A	$000	$000	$0 00	0.00
MLTX02-004EN-889	ShopDWG SubmittalforCableTension Layout	2.00	100%	100%	13 May-26	14May-26	13 May 25 A	14May-26A	$000	$000	$0 00	0.00
MLTX02-004EN-890	ShopDWG SubmittalforAirlock DoorDetails	2.00	100%	100%	13 May-26	14May-26	13 May 25 A	14May-26A	$000	$000	$0 00	0.00
MLTX02-004EN-891	ShopDWG SubmittalforEmergency ExitDetails	2.00	100%	100%	13 May-26	14May-26	13 May 25 A	14May-26A	$000	$000	$0 00	0.00
	SPORTS EQUPMENT	2.00	0%	0%	13 May-26	14May-26	13 May 25 A	14May-26A	$000	$000	$0 00	0.00
MLTX02-004EN-894	ShopDWG SubmittalforFootbal Turf Installation	2.00	100%	100%	13 May-26	14May-26	13 May 25 A	14May-26A	$000	$000	$0 00	0.00
MLTX02-004EN-895	ShopDWG SubmittalforBasketballCourtMarking	2.00	100%	100%	13 May-26	14May-26	13 May 25 A	14May-26A	$000	$000	$0 00	0.00
MLTX02-004EN-896	ShopDWG SubmittalforPadelCourtStructure	2.00	100%	100%	13 May-26	14May-26	13 May 25 A	14May-26A	$000	$000	$0 00	0.00
	MECHANCALWORKS	2000	0%	0%	08 Apr2 6	30Apr-26	08 Apr2 6A	30Apr-26A	$000	$000	$0 00	0.00
MLTX02-004EN-876	ShopDWG SubmittalforHVAC Plan	2000	100%	100%	08 Apr2 6	30Apr-26	08 Apr2 6A	30Apr-26A	$000	$000	$0 00	0.00
MLTX02-004EN-877	ShopDWG SubmittalforExhaustAirPlan	2000	100%	100%	08 Apr2 6	30Apr-26	08 Apr2 6A	30Apr-26A	$000	$000	$0 00	0.00
	ELECTRCALWORKS	8900	0%	0%	23 May-26	09Jul-26	23 May 25 A	25Aug-26A	$000	$000	$0 00	-4000

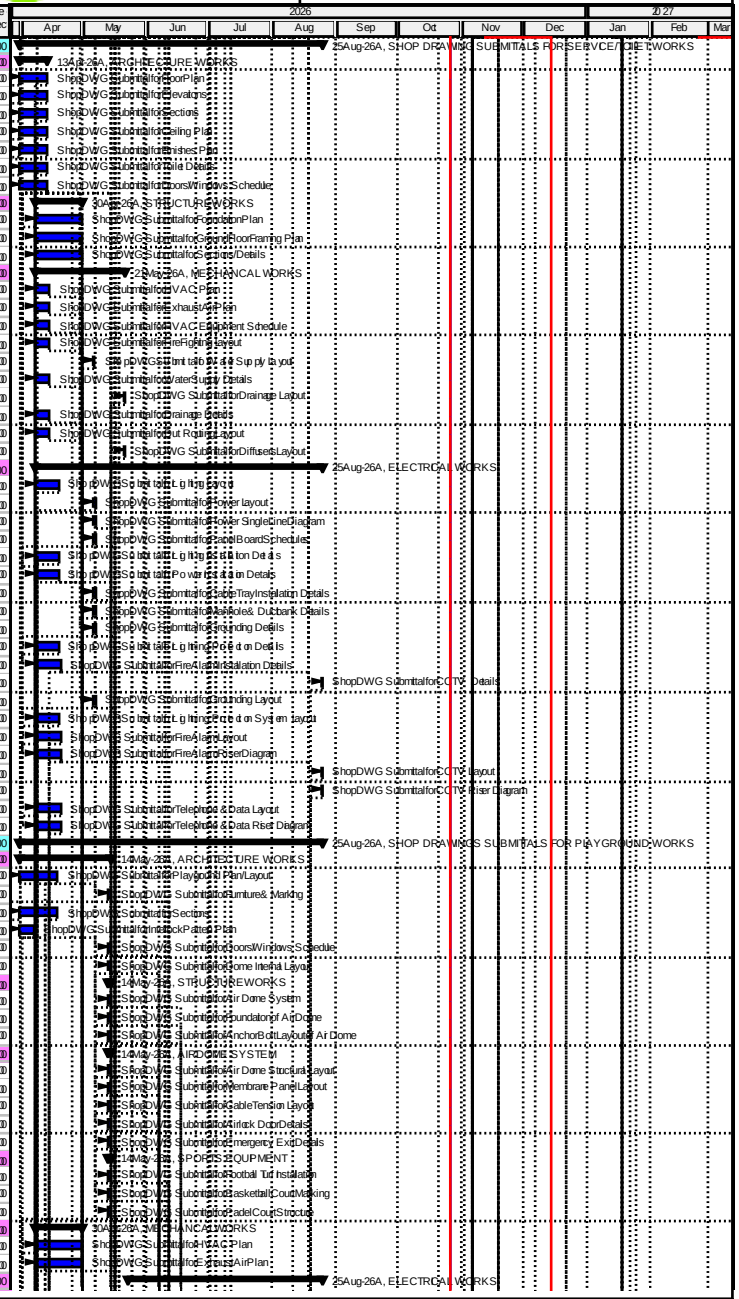


© Oracle Corporation

ActivityID	ActivityName	Orginal Duration	Schedule %	Performance% Complete	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Variance - BL Project
MLTX02-004EN-86E	ShopDWG SubmittalforLighting Layout	1.00	100%	100%	25-May-26	25May-26	25 May 26 A	25May-26A	$000	$000	$0.00	0.00
MLTX02-004EN-86E	ShopDWG SubmittalforPower layout	5.00	100%	100%	05 Jul-26	09Jul-26	08 Jul-26A	08Jul-26A	$000	$000	$0.00	4.00
MLTX02-004EN-86F	ShopDWG SubmittalforPower SingleLineDiagram	5.00	100%	100%	05 Jul-26	09Jul-26	08 Jul-26A	08Jul-26A	$000	$000	$0.00	4.00
MLTX02-004EN-86E	ShopDWG SubmittalforPanelBoardSchedules	5.00	100%	100%	05 Jul-26	09Jul-26	08 Jul-26A	08Jul-26A	$000	$000	$0.00	4.00
MLTX02-004EN-865	ShopDWG SubmittalforPower Installation Details	5.00	100%	100%	05 Jul-26	09Jul-26	08 Jul-26A	08Jul-26A	$000	$000	$0.00	4.00
MLTX02-004EN-87C	ShopDWG SubmittalforFireAlarmInstallation Details	1.00	100%	100%	23 May-26	23May-26	23 May 26 A	23May-26A	$000	$000	$0.00	0.00
MLTX02-004EN-871	ShopDWG SubmittalforCCTV Details	5.00	100%	100%	05 Jul-26	09Jul-26	25 Aug 26 A	25Aug-26A	$000	$000	$0.00	4.00
MLTX02-004EN-872	ShopDWG SubmittalforFireAlarmLayout	1.00	100%	100%	23 May-26	23May-26	23 May 26 A	23May-26A	$000	$000	$0.00	0.00
MLTX02-004EN-873	ShopDWG SubmittalforFireAlarmRiserDiagram	1.00	100%	100%	23 May-26	23May-26	23 May 26 A	23May-26A	$000	$000	$0.00	0.00
MLTX02-004EN-874	ShopDWG SubmittalforCCTV Layout	5.00	100%	100%	05 Jul-26	09Jul-26	25 Aug 26 A	25Aug-26A	$000	$000	$0.00	4.00
MLTX02-004EN-875	ShopDWG SubmittalforCCTV Riser Diagram	5.00	100%	100%	05 Jul-26	09Jul-26	25 Aug 26 A	25Aug-26A	$000	$000	$0.00	4.00
SHOP DRAWIN GSSUBMITTALS FOR LANDSCAPE WORKS		9500	0%	0%	31 Mar26	09Jul-26	31 Mar26 A	18Jul-26A	$000	$000	$0.00	-700
ARCHITECTURE WORKS		3900	0%	0%	31 Mar26	14May-26	31 Mar26 A	14May-26A	$000	$000	$0.00	0.00
MLTX02-004EN-85E	ShopDWG SubmittalforLandscape Layout	1500	100%	100%	31 Mar26	16Apr-26	31 Mar26 A	16Apr-26A	$000	$000	$0.00	0.00
MLTX02-004EN-86C	ShopDWG SubmittalforHardscape Plan	2.00	100%	100%	13 May-26	14May-26	13 May 26 A	14May-26A	$000	$000	$0.00	0.00
MLTX02-004EN-861	ShopDWG SubmittalforPlanting Plan	2.00	100%	100%	13 May-26	14May-26	13 May 26 A	14May-26A	$000	$000	$0.00	0.00
MLTX02-004EN-862	ShopDWG SubmittalforLandscape Details	2.00	100%	100%	13 May-26	14May-26	13 May 26 A	14May-26A	$000	$000	$0.00	0.00
MECHANCAL WORKS		5.00	0%	0%	05 Jul-26	09Jul-26	18 Jul-26A	18Jul-26A	$000	$000	$0.00	4.00
MLTX02-004EN-863	ShopDWG SubmittalforIrrigation Details	5.00	100%	100%	05 Jul-26	09Jul-26	18 Jul-26A	18Jul-26A	$000	$000	$0.00	4.00
MLTX02-004EN-864	ShopDWG SubmittalforIrrigation Layout	5.00	100%	100%	05 Jul-26	09Jul-26	18 Jul-26A	18Jul-26A	$000	$000	$0.00	4.00
ELECTRCAL WORKS		1.00	0%	0%	23 May-26	23May-26	23 May 26 A	23May-26A	$000	$000	$0.00	0.00
MLTX02-004EN-78E	ShopDWG SubmittalforLighting GeneralArrangement	1.00	100%	100%	23 May-26	23May-26	23 May 26 A	23May-26A	$000	$000	$0.00	0.00
MLTX02-004EN-79C	ShopDWG SubmittalforLighting NetworkLayout	1.00	100%	100%	23 May-26	23May-26	23 May 26 A	23May-26A	$000	$000	$0.00	0.00
MLTX02-004EN-791	ShopDWG SubmittalforLighting Details	1.00	100%	100%	23 May-26	23May-26	23 May 26 A	23May-26A	$000	$000	$0.00	0.00
MLTX02-004EN-792	ShopDWG SubmittalforLighting SingleLine Diagram	1.00	100%	100%	23 May-26	23May-26	23 May 26 A	23May-26A	$000	$000	$0.00	0.00
SHOP DRAWINGS APPROVALS		13800	0%	0%	07 Apr26	21Jul-26	07 Apr26 A	26Aug-26A	$000	$000	$0.00	-3100
SHOP DRAWIN GAPPROVALFOR EARTHINGW ORKS		7100	0%	0%	07 Apr26	01Jul-26	07 Apr26 A	01Jul-26A	$000	$000	$0.00	0.00
MLTX02-004EN-11260	ShopDWG AppovalforLayoutPlan	1.00	100%	100%	21 May-26	21May-26	21 May 26 A	21May-26A	$000	$000	$0.00	0.00
MLTX02-004EN-11270	ShopDWG AppovalforSettingOut	1700	100%	100%	07 Apr26	26Apr-26	07 Apr26 A	26Apr-26A	$000	$000	$0.00	0.00
MLTX02-004EN-11280	ShopDWG AppovalforGadingLayoutPlan	1.00	100%	100%	21 May-26	21May-26	21 May 26 A	21May-26A	$000	$000	$0.00	0.00
MLTX02-004EN-11290	ShopDWG AppovalforCub SettingOut Points	1.00	100%	100%	23 May-26	23May-26	23 May 26 A	23May-26A	$000	$000	$0.00	0.00
MLTX02-004EN-11300	ShopDWG AppovalforSigning& Marking Layout Plan	1.00	100%	100%	01 Jul-26	01Jul-26	01 Jul-26A	01Jul-26A	$000	$000	$0.00	0.00
MLTX02-004EN-11310	ShopDWG AppovalforStandards Details	1.00	100%	100%	21 May-26	21May-26	21 May 26 A	21May-26A	$000	$000	$0.00	0.00
SHOP DRAWIN GAPPROVALFOR SERVIC EDUCTWORKS		13200	0%	0%	14 Apr26	21Jul-26	14 Apr26 A	26Aug-26A	$000	$000	$0.00	-3100
ARCHITECTURE WORKS		9.00	0%	0%	14 Apr26	23Apr-26	14 Apr26 A	24Apr-26A	$000	$000	$0.00	0.00
MLTX02-004EN-113	ShopDWG AppovalforFloorPlan	9.00	100%	100%	14 Apr26	23Apr-26	14 Apr26 A	24Apr-26A	$000	$000	$0.00	0.00
MLTX02-004EN-113	ShopDWG AppovalforElevations	9.00	100%	100%	14 Apr26	23Apr-26	14 Apr26 A	24Apr-26A	$000	$000	$0.00	0.00
MLTX02-004EN-113	ShopDWG AppovalforSections	9.00	100%	100%	14 Apr26	23Apr-26	14 Apr26 A	24Apr-26A	$000	$000	$0.00	0.00
MLTX02-004EN-113	ShopDWG AppovalforCeilingPlan	9.00	100%	100%	14 Apr26	23Apr-26	14 Apr26 A	24Apr-26A	$000	$000	$0.00	0.00
MLTX02-004EN-114	ShopDWG AppovalforFinishes Plan	9.00	100%	100%	14 Apr26	23Apr-26	14 Apr26 A	24Apr-26A	$000	$000	$0.00	0.00
MLTX02-004EN-114	ShopDWG AppovalforToiletDetails	9.00	100%	100%	14 Apr26	23Apr-26	14 Apr26 A	24Apr-26A	$000	$000	$0.00	0.00
MLTX02-004EN-114	ShopDWG AppovalforDoors/WindowsSchedule	9.00	100%	100%	14 Apr26	23Apr-26	14 Apr26 A	24Apr-26A	$000	$000	$0.00	0.00
STRUCTUREWORKS		1.00	0%	0%	07 May-26	07May-26	07 May 26 A	07May-26A	$000	$000	$0.00	0.00
MLTX02-004EN-114	ShopDWG AppovalforFoundation Plan	1.00	100%	100%	07 May-26	07May-26	07 May 26 A	07May-26A	$000	$000	$0.00	0.00
MLTX02-004EN-114	ShopDWG AppovalforGound FloorFraming Plan	1.00	100%	100%	07 May-26	07May-26	07 May 26 A	07May-26A	$000	$000	$0.00	0.00
MLTX02-004EN-114	ShopDWG AppovalforSectionsDetails	1.00	100%	100%	07 May-26	07May-26	07 May 26 A	07May-26A	$000	$000	$0.00	0.00
MECHANCAL WORKS		1300	0%	0%	07 May-26	21May-26	07 May 26 A	21May-26A	$000	$000	$0.00	0.00
MLTX02-004EN-114	ShopDWG AppovalforHVACPlan	1.00	100%	100%	07 May-26	07May-26	07 May 26 A	07May-26A	$000	$000	$0.00	0.00
MLTX02-004EN-114	ShopDWG AppovalforExhaustAir Plan	1.00	100%	100%	07 May-26	07May-26	07 May 26 A	07May-26A	$000	$000	$0.00	0.00
MLTX02-004EN-114	ShopDWG AppovalforHVACEquipment Schedule	4.00	100%	100%	07 May-26	11May-26	07 May 26 A	11May-26A	$000	$000	$0.00	0.00
MLTX02-004EN-114	ShopDWG AppovalforFire fighting Layout	1.00	100%	100%	07 May-26	07May-26	07 May 26 A	07May-26A	$000	$000	$0.00	0.00
MLTX02-004EN-115	ShopDWG AppovalforWaterSupplyLayout	1.00	100%	100%	07 May-26	07May-26	07 May 26 A	07May-26A	$000	$000	$0.00	0.00
MLTX02-004EN-115	ShopDWG AppovalforWaterSupplyDetails	1.00	100%	100%	07 May-26	07May-26	07 May 26 A	07May-26A	$000	$000	$0.00	0.00
MLTX02-004EN-115	ShopDWG AppovalforDrainageLayout	1.00	100%	100%	21 May-26	21May-26	21 May 26 A	21May-26A	$000	$000	$0.00	0.00
MLTX02-004EN-115	ShopDWG AppovalforDrainageDetails	1.00	100%	100%	07 May-26	07May-26	07 May 26 A	07May-26A	$000	$000	$0.00	0.00
MLTX02-004EN-120	ShopDWG AppovalforDuct RodingLayout	1.00	100%	100%	07 May-26	07May-26	07 May 26 A	07May-26A	$000	$000	$0.00	0.00
MLTX02-004EN-120	ShopDWG AppovalforDiffusers Layout	1.00	100%	100%	21 May-26	21May-26	21 May 26 A	21May-26A	$000	$000	$0.00	0.00
ELECTRCAL WORKS		13100	0%	0%	15 Apr26	21Jul-26	15 Apr26 A	26Aug-26A	$000	$000	$0.00	-3100
MLTX02-004EN-115	ShopDWG Appovalfor lighting Layout	1000	100%	100%	15 Apr26	26Apr-26	15 Apr26 A	26Apr-26A	$000	$000	$0.00	0.00
MLTX02-004EN-115	ShopDWG Appovalfor Power Layout	1000	100%	100%	15 Apr26	26Apr-26	15 Apr26 A	26Apr-26A	$000	$000	$0.00	0.00
MLTX02-004EN-115	ShopDWG Appovalfor Paver Single line Diagram	1.00	100%	100%	23 May-26	23May-26	23 May 26 A	23May-26A	$000	$000	$0.00	0.00
MLTX02-004EN-115	ShopDWG Appovalfor Panel Board Schedules	1.00	100%	100%	23 May-26	23May-26	23 May 26 A	23May-26A	$000	$000	$0.00	0.00
MLTX02-004EN-115	ShopDWG Appovalfor lighting InstallbtionDetails	1000	100%	100%	15 Apr26	26Apr-26	15 Apr26 A	26Apr-26A	$000	$000	$0.00	0.00
MLTX02-004EN-115	ShopDWG Appovalfor Paver InstallbtionDetails	1.00	100%	100%	23 May-26	23May-26	23 May 26 A	23May-26A	$000	$000	$0.00	0.00
MLTX02-004EN-116	ShopDWG Appovalfor Cable Tray InstallbtionDetails	1.00	100%	100%	23 May-26	23May-26	23 May 26 A	23May-26A	$000	$000	$0.00	0.00
MLTX02-004EN-116	ShopDWG Appovalfor Manhole& Ducttank Details	1.00	100%	100%	23 May-26	23May-26	23 May 26 A	23May-26A	$000	$000	$0.00	0.00
MLTX02-004EN-116	ShopDWG Appovalfor Gounding Details	1.00	100%	100%	23 May-26	23May-26	23 May 26 A	23May-26A	$000	$000	$0.00	0.00
MLTX02-004EN-116	ShopDWG Appovalfor Lightning Potection Details	1000	100%	100%	15 Apr26	26Apr-26	15 Apr26 A	26Apr-26A	$000	$000	$0.00	0.00
MLTX02-004EN-116	ShopDWG Appovalfor fire Alarm Instalation Details	6.00	100%	100%	21 May-26	27Apr-26	21 Apr26 A	27Apr-26A	$000	$000	$0.00	0.00
MLTX02-004EN-116	ShopDWG Appovalfor CCTV Details	1000	100%	100%	11 Jul-26	21Jul-26	26 Aug 26 A	26Aug-26A	$000	$000	$0.00	9.00
MLTX02-004EN-116	ShopDWG Appovalfor Gounding Layout	1.00	100%	100%	23 May-26	23May-26	23 May 26 A	23May-26A	$000	$000	$0.00	0.00

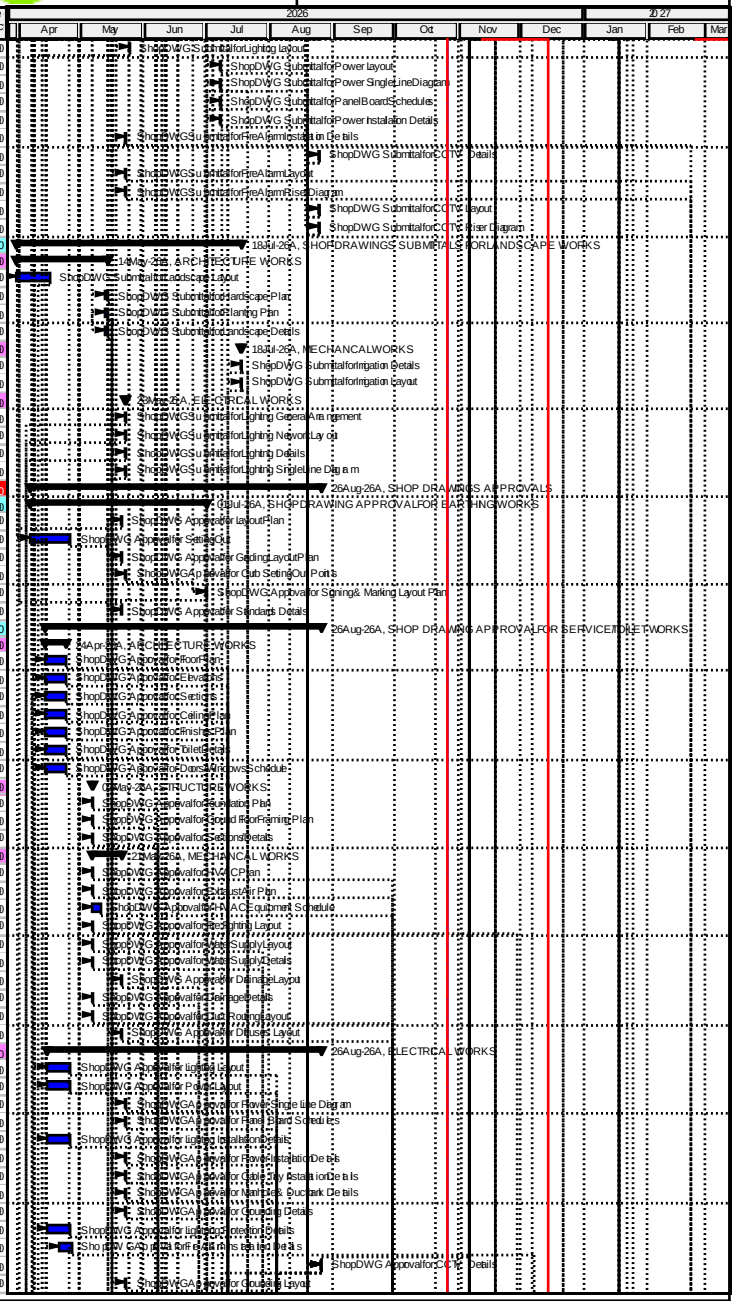


© Oracle Corporation

ActivityID	ActivityName	Orginal Duration	Schedule %	Performance% Complete	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Variance - BL Project
MLTX02-004EN-1160	ShopDWG Appovalfor Lightning Protection System Layout	1000	100%	100%	15 Apr 26	26Apr-26	15 Apr 26 A	26Apr-26A	$000	$000	$0.00	0.00
MLTX02-004EN-1161	ShopDWG Appovalfor fire Alarm layout	6.00	100%	100%	21 Apr 26	27Apr-26	21 Apr 26 A	27Apr-26A	$000	$000	$0.00	0.00
MLTX02-004EN-1162	ShopDWG Appovalfor fire Alarm Riser Diagram	6.00	100%	100%	21 Apr 26	27Apr-26	21 Apr 26 A	27Apr-26A	$000	$000	$0.00	0.00
MLTX02-004EN-1170	ShopDWG Appovalfor CCTV Layout	1000	100%	100%	11 Jul-25	21Jul-26	25 Aug 25 A	26Aug-26A	$000	$000	$0.00	9.00
MLTX02-004EN-1171	ShopDWG Appovalfor CCTV RiserDiagram	1000	100%	100%	11 Jul-25	21Jul-26	25 Aug 25 A	26Aug-26A	$000	$000	$0.00	9.00
MLTX02-004EN-1172	ShopDWG Appovalfor Telephone & Data Layout	6.00	100%	100%	21 Apr 26	27Apr-26	21 Apr 26 A	27Apr-26A	$000	$000	$0.00	0.00
MLTX02-004EN-1173	ShopDWG Appovalfor Telephone & Data Riser Diagram	6.00	100%	100%	21 Apr 26	27Apr-26	21 Apr 26 A	27Apr-26A	$000	$000	$0.00	0.00
SHOP DRAWIN GSAPPROVALFOR PLAYGROUND WORKS		13700	0%	0%	08 Apr 26	21Jul-26	08 Apr 26 A	26Aug-26A	$000	$000	$0.00	-3100
ARCHITECTURE WORKS		5900	0%	0%	08 Apr 26	18Jun-26	08 Apr 26 A	18Jun-26A	$000	$000	$0.00	0.00
MLTX02-004EN-1150	ShopDWG Appovalfor Playground Plan/Layout	5.00	100%	100%	19 Apr 26	23Apr-26	19 Apr 26 A	24Apr-26A	$000	$000	$0.00	0.00
MLTX02-004EN-1151	ShopDWG Appovalfor furniture & Marking	1.00	100%	100%	18 Jun-26	18Jun-26	18 Jun 26 A	18Jun-26A	$000	$000	$0.00	0.00
MLTX02-004EN-1152	ShopDWG Appovalfor Sections	5.00	100%	100%	19 Apr 26	23Apr-26	19 Apr 26 A	24Apr-26A	$000	$000	$0.00	0.00
MLTX02-004EN-1153	ShopDWG Appovalfor Interlock PatternPlan	1000	100%	100%	08 Apr 26	19Apr-26	08 Apr 26 A	19Apr-26A	$000	$000	$0.00	0.00
MLTX02-004EN-1154	ShopDWG Appovalfor Doors/Windows Schedule	1.00	100%	100%	13 Jun 26	13Jun-26	13 Jun 26 A	13Jun-26A	$000	$000	$0.00	0.00
MLTX02-004EN-1155	ShopDWG Appovalfor Dome InternalLayout	1.00	100%	100%	13 Jun 26	13Jun-26	13 Jun 26 A	13Jun-26A	$000	$000	$0.00	0.00
STRUCTUREWORKS		1.00	0%	0%	24 Jun 26	24Jun-26	24 Jun 26 A	24Jun-26A	$000	$000	$0.00	0.00
MLTX02-004EN-1156	ShopDWG Appovalfor Air DomeSystem	1.00	100%	100%	24 Jun 26	24Jun-26	24 Jun 26 A	24Jun-26A	$000	$000	$0.00	0.00
MLTX02-004EN-1157	ShopDWG Appovalfor Foundation ofAirDome	1.00	100%	100%	24 Jun 26	24Jun-26	24 Jun 26 A	24Jun-26A	$000	$000	$0.00	0.00
MLTX02-004EN-1158	ShopDWG Appovalfor Foundation ofAirDome	1.00	100%	100%	24 Jun 26	24Jun-26	24 Jun 26 A	24Jun-26A	$000	$000	$0.00	0.00
MLTX02-004EN-1159	ShopDWG Appovalfor Anchor Bolt layoutof AirDome	1.00	100%	100%	24 Jun 26	24Jun-26	24 Jun 26 A	24Jun-26A	$000	$000	$0.00	0.00
AIRDOMESYS TEM		1.00	0%	0%	13 Jun 26	13Jun-26	13 Jun 26 A	13Jun-26A	$000	$000	$0.00	0.00
MLTX02-004EN-1200	ShopDWG Appovalfor Air DomeStructuralLayout	1.00	100%	100%	13 Jun 26	13Jun-26	13 Jun 26 A	13Jun-26A	$000	$000	$0.00	0.00
MLTX02-004EN-1201	ShopDWG Appovalfor MembranePanelLayout	1.00	100%	100%	13 Jun 26	13Jun-26	13 Jun 26 A	13Jun-26A	$000	$000	$0.00	0.00
MLTX02-004EN-1202	ShopDWG Appovalfor Cable TensionLayout	1.00	100%	100%	13 Jun 26	13Jun-26	13 Jun 26 A	13Jun-26A	$000	$000	$0.00	0.00
MLTX02-004EN-1203	ShopDWG Appovalfor AirlockDoorDetails	1.00	100%	100%	13 Jun 26	13Jun-26	13 Jun 26 A	13Jun-26A	$000	$000	$0.00	0.00
MLTX02-004EN-1204	ShopDWG Appovalfor EmergencyExitDetails	1.00	100%	100%	13 Jun 26	13Jun-26	13 Jun 26 A	13Jun-26A	$000	$000	$0.00	0.00
SPORTS EQUIPMENT		1.00	0%	0%	18 Jun 26	18Jun-26	18 Jun 26 A	18Jun-26A	$000	$000	$0.00	0.00
MLTX02-004EN-1205	ShopDWG Appovalfor Rootbal Tuf Installation	1.00	100%	100%	18 Jun 26	18Jun-26	18 Jun 26 A	18Jun-26A	$000	$000	$0.00	0.00
MLTX02-004EN-1206	ShopDWG Appovalfor Basketball Court Making	1.00	100%	100%	18 Jun 26	18Jun-26	18 Jun 26 A	18Jun-26A	$000	$000	$0.00	0.00
MLTX02-004EN-1207	ShopDWG Appovalfor Padel Court Stucture	1.00	100%	100%	18 Jun 26	18Jun-26	18 Jun 26 A	18Jun-26A	$000	$000	$0.00	0.00
MECHANCAL WORKS		1.00	0%	0%	07 May-26	07May-26	07 May 26 A	07May-26A	$000	$000	$0.00	0.00
MLTX02-004EN-1180	ShopDWG Appovalfor HVACPlan	1.00	100%	100%	07 May-26	07May-26	07 May 26 A	07May-26A	$000	$000	$0.00	0.00
MLTX02-004EN-1181	ShopDWG Appovalfor ExhaustAir Plan	1.00	100%	100%	07 May-26	07May-26	07 May 26 A	07May-26A	$000	$000	$0.00	0.00
ELECTRCAL WORKS		13100	0%	0%	15 Apr 26	21Jul-26	15 Apr 26 A	26Aug-26A	$000	$000	$0.00	-3100
MLTX02-004EN-1182	ShopDWG Appovalfor Lighting Layout	1000	100%	100%	15 Apr 26	26Apr-26	15 Apr 26 A	26Apr-26A	$000	$000	$0.00	0.00
MLTX02-004EN-1183	ShopDWG Appovalfor Paver Layout	1000	100%	100%	15 Apr 26	26Apr-26	15 Apr 26 A	26Apr-26A	$000	$000	$0.00	0.00
MLTX02-004EN-1184	ShopDWG Appovalfor Power Single line Diagram	1000	100%	100%	11 Jul-25	21Jul-26	08 Jul-26A	08Jul-26A	$000	$000	$0.00	9.00
MLTX02-004EN-1185	ShopDWG Appovalfor Panel Board Schedules	1000	100%	100%	11 Jul-25	21Jul-26	08 Jul-26A	08Jul-26A	$000	$000	$0.00	9.00
MLTX02-004EN-1186	ShopDWG Appovalfor Paver InstallationDetails	1000	100%	100%	15 Apr 26	26Apr-26	15 Apr 26 A	26Apr-26A	$000	$000	$0.00	0.00
MLTX02-004EN-1187	ShopDWG Appovalfor CCTV Details	1000	100%	100%	11 Jul-25	21Jul-26	25 Aug 25 A	26Aug-26A	$000	$000	$0.00	9.00
MLTX02-004EN-1188	ShopDWG Appovalfor CCTV Layout	1000	100%	100%	11 Jul-25	21Jul-26	25 Aug 25 A	26Aug-26A	$000	$000	$0.00	9.00
MLTX02-004EN-1189	ShopDWG Appovalfor CCTV RiserDiagram	1000	100%	100%	11 Jul-25	21Jul-26	25 Aug 25 A	26Aug-26A	$000	$000	$0.00	9.00
SHOP DRAWIN GSAPPROVALFOR LANDSCAPE WORKS		9100	0%	0%	11 Apr 26	21Jul-26	11 Apr 26 A	18Jul-26A	$000	$000	$0.00	3.00
ARCHITECTURE WORKS		3100	0%	0%	18 Apr 26	23May-26	17 Apr 26 A	23May-26A	$000	$000	$0.00	0.00
MLTX02-004EN-1170	ShopDWG Appovalfor landscape Layout	6.00	100%	100%	18 Apr 26	23Apr-26	17 Apr 26 A	24Apr-26A	$000	$000	$0.00	0.00
MLTX02-004EN-1171	ShopDWG Appovalfor Hardscape Plan	1.00	100%	100%	23 May-26	23May-26	23 May 25 A	23May-26A	$000	$000	$0.00	0.00
MLTX02-004EN-1172	ShopDWG Appovalfor Planting Plan	1.00	100%	100%	23 May-26	23May-26	23 May 25 A	23May-26A	$000	$000	$0.00	0.00
MLTX02-004EN-1173	ShopDWG Appovalfor landscape Details	1.00	100%	100%	23 May-26	23May-26	23 May 25 A	23May-26A	$000	$000	$0.00	0.00
MECHANCAL WORKS		1000	0%	0%	11 Jul-25	21Jul-26	18 Jul-26A	18Jul-26A	$000	$000	$0.00	9.00
MLTX02-004EN-1174	ShopDWG Appovalfor IrrigationDetails	1000	100%	100%	11 Jul-25	21Jul-26	18 Jul-26A	18Jul-26A	$000	$000	$0.00	9.00
MLTX02-004EN-1175	ShopDWG Appovalfor IrrigationLayout	1000	100%	100%	11 Jul-25	21Jul-26	18 Jul-26A	18Jul-26A	$000	$000	$0.00	9.00
ELECTRCAL WORKS		3700	0%	0%	11 Apr 26	23May-26	11 Apr 26 A	23May-26A	$000	$000	$0.00	0.00
MLTX02-004EN-1130	ShopDWG Appovalfor lighting General Arrangement	1000	100%	100%	11 Apr 26	21Apr-26	11 Apr 26 A	21Apr-26A	$000	$000	$0.00	0.00
MLTX02-004EN-1131	ShopDWG Appovalfor lighting Network Layout	1000	100%	100%	11 Apr 26	21Apr-26	11 Apr 26 A	21Apr-26A	$000	$000	$0.00	0.00
MLTX02-004EN-1132	ShopDWG Appovalfor lighting Details	1000	100%	100%	11 Apr 26	21Apr-26	11 Apr 26 A	21Apr-26A	$000	$000	$0.00	0.00
MLTX02-004EN-1133	ShopDWG Appovalfor lighting Single Line Diagram	1.00	100%	100%	23 May-26	23May-26	23 May 25 A	23May-26A	$000	$000	$0.00	0.00
METHOD STATEMENTS		19100	0%	0%	31 Mar 26	02Aug-26	31 Mar 26 A	12Nov-26	$000	$000	$0.00	-8700
METHOD STATEMENTS UBMITTAL		18100	0%	0%	31 Mar 26	18Jul-26	31 Mar 26 A	01Nov-26	$000	$000	$0.00	-9000
CIVL WORKS		4500	0%	0%	31 Mar 26	21May-26	31 Mar 26 A	21May-26A	$000	$000	$0.00	0.00
MLTX02-004EN-7930	Preparation & Submissionof MethodStatement forEarthwork	1700	100%	100%	31 Mar 26	19Apr-26	31 Mar 26 A	19Apr-26A	$000	$000	$0.00	0.00
MLTX02-004EN-7940	Preparation & Submissionof MethodStatement forConcete Works	1.00	100%	100%	21 May-26	21May-26	21 May 25 A	21May-26A	$000	$000	$0.00	0.00
MLTX02-004EN-7950	Preparation & Submissionof MethodStatement forWaterproding	2200	100%	100%	31 Mar 26	25Apr-26	31 Mar 26 A	25Apr-26A	$000	$000	$0.00	0.00
ARCHITECTURE WORKS		13200	0%	0%	31 May-26	11Jul-26	31 May 25 A	01Nov-26	$000	$000	$0.00	-9600
MLTX02-004EN-8060	Preparation & Submissionof MethodStatement forFenceWorks	5.00	100%	0%	05 Jul-25	09Jul-26	27 Oct 26	01Nov-26	$000	$000	$0.00	0.00
MLTX02-004EN-7980	Preparation & Submissionof MethodStatement forPlasteringWorks	1.00	100%	100%	16 Jun 26	16Jun-26	16 Jun 26 A	16Jun-26A	$000	$000	$0.00	0.00
MLTX02-004EN-7990	Preparation & Submissionof MethodStatement forMasonary Waks	1.00	100%	100%	16 Jun 26	16Jun-26	16 Jun 26 A	16Jun-26A	$000	$000	$0.00	0.00
MLTX02-004EN-8000	Preparation & Submissionof MethodStatement forTilingWorks	1.00	100%	100%	06 Jun 26	06Jun-26	06 Jun 26 A	06Jun-26A	$000	$000	$0.00	0.00
MLTX02-004EN-8010	Preparation & Submissionof MethodStatement forSeats/BenchesWorks	1.00	100%	100%	18 Jun 26	18Jun-26	18 Jun 26 A	18Jun-26A	$000	$000	$0.00	0.00
MLTX02-004EN-8020	Preparation & Submissionof MethodStatement forDoors/Windows Works	1.00	100%	100%	06 Jun 26	06Jun-26	06 Jun 26 A	06Jun-26A	$000	$000	$0.00	0.00
MLTX02-004EN-8030	Preparation & Submissionof MethodStatement forInterlock/Curbstone Works	1.00	100%	100%	31 May-26	31May-26	31 May 25 A	31May-26A	$000	$000	$0.00	0.00
MLTX02-004EN-8040	Preparation & Submissionof MethodStatement forParking Works	1.00	100%	100%	31 May-26	31May-26	31 May 25 A	31May-26A	$000	$000	$0.00	0.00

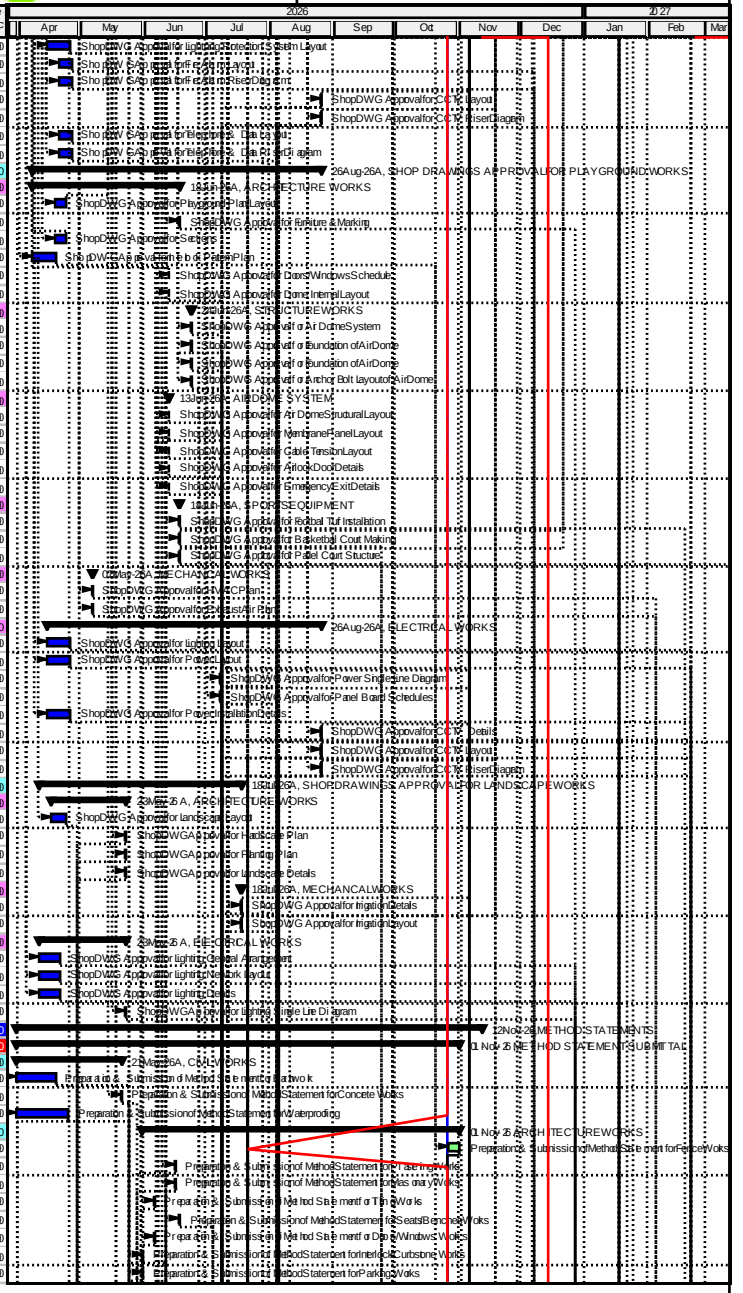


© Oracle Corporation

ActivityID	ActivityName	Orginal Duration	Schedule %	Performance% Complete	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Variance - BL Project
MLTX-02-004EN-8050	Preparation & Submissionof MethodStatement forSoftScapeWorks	5.00	100%	100%	05-Jul-26	09-Jul-26	11-Jul-26A	11-Jul-26A	$000	$000	$0.00	4.00
MLTX-02-004EN-8070	Preparation & Submissionof MethodStatement forAirDome Works	5.00	100%	100%	05-Jul-26	09-Jul-26	17-Aug-26A	17-Aug-26A	$000	$000	$0.00	4.00
MLTX-02-004EN-8080	Preparation & Submissionof MethodStatement forMetalWorks	6.00	100%	100%	05-Jul-26	11-Jul-26	11-Jul-26A	11-Jul-26A	$000	$000	$0.00	5.00
MLTX-02-004EN-8090	Preparation & Submissionof MethodStatement forPartitions Works	5.00	100%	100%	05-Jul-26	09-Jul-26	15-Jul-26A	15-Jul-26A	$000	$000	$0.00	4.00
MLTX-02-004EN-8100	Preparation & Submissionof MethodStatement forGypsumBoardWorks	1.00	100%	100%	13-Jun-26	13-Jun-26	13-Jun-26A	13-Jun-26A	$000	$000	$0.00	0.00
MECHANICALWORKS		4800	0%	0%	07-Apr-26	04-Jun-26	07-Apr-26A	04-Jun-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-8110	Preparation & Submissionof MethodStatement forSewageDrainage System	1.00	100%	100%	31-May-26	31-May-26	31-May-26A	31-May-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-8120	Preparation & Submissionof MethodStatement forWater Supply System	1.00	100%	100%	04-Jun-26	04-Jun-26	04-Jun-26A	04-Jun-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-8130	Preparation & Submissionof MethodStatement forFire FightingSystem	6.00	100%	100%	07-Apr-26	13-Apr-26	07-Apr-26A	14-Apr-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-8140	Preparation & Submissionof MethodStatement forIrrigation System	0.00	100%	100%	04-Jun-26	04-Jun-26	04-Jun-26A	04-Jun-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-8150	Preparation & Submissionof MethodStatement forHVAC System	0.00	100%	100%	04-Jun-26	04-Jun-26	04-Jun-26A	04-Jun-26A	$000	$000	$0.00	0.00
ELECTRICAL WORKS		5800	0%	0%	18-Jun-26	18-Jul-26	18-Jun-26A	12-Aug-26A	$000	$000	$0.00	-2200
MLTX-02-004EN-7960	Preparation & Submissionof MethodStatement forElecticalConduits/PullingWorks	1.00	100%	100%	18-Jun-26	18-Jun-26	18-Jun-26A	18-Jun-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-7970	Preparation & Submissionof MethodStatement forLightingPoles Installation	1.00	100%	100%	18-Jun-26	18-Jun-26	18-Jun-26A	18-Jun-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-8160	Preparation & Submissionof MethodStatement forTelecommunication& DataSyste	7.00	100%	100%	11-Jul-26	18-Jul-26	15-Jul-26A	15-Jul-26A	$000	$000	$0.00	6.00
MLTX-02-004EN-8170	Preparation & Submissionof MethodStatement forCCTV System	7.00	100%	100%	11-Jul-26	18-Jul-26	22-Jul-26A	22-Jul-26A	$000	$000	$0.00	6.00
MLTX-02-004EN-8180	Preparation & Submissionof MethodStatement forLightingWorks	1.00	100%	100%	18-Jun-26	18-Jun-26	18-Jun-26A	18-Jun-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-8190	Preparation & Submissionof MethodStatement forEarthing/lightning Works	1.00	100%	100%	18-Jun-26	18-Jun-26	18-Jun-26A	18-Jun-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-8200	Preparation & Submissionof MethodStatement forPanelBoardsWorks	6.00	100%	100%	05-Jul-26	11-Jul-26	12-Aug-26A	12-Aug-26A	$000	$000	$0.00	5.00
METHOD STATEMENT APPROVAL		17800	0%	0%	15-Apr-26	02-Aug-26	15-Apr-26A	12-Nov-26	$000	$000	$0.00	-8700
CIVL WORKS		1.00	0%	0%	31-May-26	31-May-26	31-May-26A	31-May-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-10990	Appoval of Method Statementfor Earthwok	1.00	100%	100%	31-May-26	31-May-26	31-May-26A	31-May-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-11000	Appoval of Method Statementfor Concrete Woks	1.00	100%	100%	31-May-26	31-May-26	31-May-26A	31-May-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-11010	Appoval of Method Statementfor Wateproofing	1.00	100%	100%	31-May-26	31-May-26	31-May-26A	31-May-26A	$000	$000	$0.00	0.00
ARCHITECTURE WORKS		14200	0%	0%	31-May-26	21-Jul-26	31-May-26A	12-Nov-26	$000	$000	$0.00	-9700
MLTX-02-004EN-11120	Appoval of Method Statementfor fence Works	1000	100%	0%	11-Jul-26	21-Jul-26	02-Nov-26	12-Nov-26	$000	$000	$0.00	0.00
MLTX-02-004EN-11040	Appoval of Method Statementfor Plasteing Works	1.00	100%	100%	18-Jun-26	18-Jun-26	18-Jun-26A	18-Jun-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-11050	Appoval of Method Statementfor MasonaryWorks	1.00	100%	100%	18-Jun-26	18-Jun-26	18-Jun-26A	18-Jun-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-11060	Appoval of Method Statementfor Tiling Works	1.00	100%	100%	06-Jun-26	06-Jun-26	06-Jun-26A	06-Jun-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-11070	Appoval of Method Statementfor Seats/Benches Works	5.00	100%	100%	05-Jul-26	09-Jul-26	11-Jul-26A	11-Jul-26A	$000	$000	$0.00	4.00
MLTX-02-004EN-11080	Appoval of Method Statementfor Doors/WndowsWorks	1.00	100%	100%	06-Jun-26	06-Jun-26	06-Jun-26A	06-Jun-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-11090	Appoval of Method Statementfor Intelock/Curbstore Works	1.00	100%	100%	31-May-26	31-May-26	31-May-26A	31-May-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-11100	Appoval of Method Statementfor ParkingWorks	1.00	100%	100%	31-May-26	31-May-26	31-May-26A	31-May-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-11110	Appoval of Method Statementfor Soft Scape Works	1000	100%	100%	11-Jul-26	21-Jul-26	11-Jul-26A	11-Jul-26A	$000	$000	$0.00	9.00
MLTX-02-004EN-11130	Appoval of Method Statementfor Air DomeWorks	1000	100%	100%	11-Jul-26	21-Jul-26	27-Aug-26A	27-Aug-26A	$000	$000	$0.00	9.00
MLTX-02-004EN-11140	Appoval of Method Statementfor PartitionsWorks	1000	100%	100%	11-Jul-26	21-Jul-26	18-Jul-26A	18-Jul-26A	$000	$000	$0.00	9.00
MLTX-02-004EN-11150	Appoval of Method Statementfor Gypsum Board Woks	1.00	100%	100%	18-Jun-26	18-Jun-26	18-Jun-26A	18-Jun-26A	$000	$000	$0.00	0.00
MECHANICALWORKS		4700	0%	0%	15-Apr-26	11-Jun-26	15-Apr-26A	11-Jun-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-11160	Appoval of Method Statementfor Sewage/DainageSystem	1.00	100%	100%	11-Jun-26	11-Jun-26	11-Jun-26A	11-Jun-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-11170	Appoval of Method Statementfor WaterSupplySystem	1.00	100%	100%	11-Jun-26	11-Jun-26	11-Jun-26A	11-Jun-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-11180	Appoval of Method Statementfor FireFighting System	1000	100%	100%	15-Apr-26	26-Apr-26	15-Apr-26A	26-Apr-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-11190	Appoval of Method Statementfor IrrigationSystem	1.00	100%	100%	11-Jun-26	11-Jun-26	11-Jun-26A	11-Jun-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-11200	Appoval of Method Statementfor HVAC System	1.00	100%	100%	11-Jun-26	11-Jun-26	11-Jun-26A	11-Jun-26A	$000	$000	$0.00	0.00
ELECTRICAL WORKS		4900	0%	0%	05-Jul-26	02-Aug-26	11-Jul-26A	15-Aug-26A	$000	$000	$0.00	-600
MLTX-02-004EN-11020	Appoval of Method Statementfor ElecticalConduits/Pulling Works	5.00	100%	100%	05-Jul-26	09-Jul-26	11-Jul-26A	11-Jul-26A	$000	$000	$0.00	4.00
MLTX-02-004EN-11030	Appoval of Method Statementfor Lighting Poles Installaion	1000	100%	100%	05-Jul-26	15-Jul-26	11-Jul-26A	11-Jul-26A	$000	$000	$0.00	9.00
MLTX-02-004EN-11210	Appoval of Method Statementfor Telecommunication & Data System	1000	100%	100%	22-Jul-26	02-Aug-26	15-Jul-26A	15-Jul-26A	$000	$000	$0.00	9.00
MLTX-02-004EN-11220	Appoval of Method Statementfor CCTV System	1000	100%	100%	19-Jul-26	29-Jul-26	22-Jul-26A	22-Jul-26A	$000	$000	$0.00	9.00
MLTX-02-004EN-11230	Appoval of Method Statementfor Lighting Works	1000	100%	100%	05-Jul-26	15-Jul-26	11-Jul-26A	11-Jul-26A	$000	$000	$0.00	9.00
MLTX-02-004EN-11240	Appoval of Method Statementfor Earthing/LightningWorks	1000	100%	100%	05-Jul-26	15-Jul-26	11-Jul-26A	11-Jul-26A	$000	$000	$0.00	9.00
MLTX-02-004EN-11250	Appoval of Method Statementfor Panel Boards Works	1000	100%	100%	12-Jul-26	22-Jul-26	15-Aug-26A	15-Aug-26A	$000	$000	$0.00	9.00
PRE-QUALIFICATION& MATERIAL		18300	0%	0%	31-Mar-26	18-Jul-26	31-Mar-26A	03-Nov-26	$000	$000	$0.00	-9200
PRE-QUALIFICATION		4500	0%	0%	31-Mar-26	21-May-26	31-Mar-26A	21-May-26A	$000	$000	$0.00	0.00
TOILETSERVICEWORKS		1800	0%	0%	31-Mar-26	20-Apr-26	31-Mar-26A	20-Apr-26A	$000	$000	$0.00	0.00
STEELREINFORCEMENT		1200	0%	0%	31-Mar-26	13-Apr-26	31-Mar-26A	13-Apr-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-999	PreQualifcation SubmittalforSteelReinforcement	1100	100%	100%	31-Mar-26	12-Apr-26	31-Mar-26A	12-Apr-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-101	PreQualifcation Appovalfor SteelReinforcement	2.00	100%	100%	12-Apr-26	13-Apr-26	12-Apr-26A	13-Apr-26A	$000	$000	$0.00	0.00
READY MIXCONCRETE		1800	0%	0%	31-Mar-26	20-Apr-26	31-Mar-26A	20-Apr-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-100	PreQualifcation SubmittalforReady Mixed Concrete	1400	100%	100%	31-Mar-26	15-Apr-26	31-Mar-26A	15-Apr-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-100	PreQualifcation Appovalof Ready Mixed Concete	5.00	100%	100%	15-Apr-26	20-Apr-26	15-Apr-26A	20-Apr-26A	$000	$000	$0.00	0.00
CONCRETE BLOCKS		1800	0%	0%	31-Mar-26	20-Apr-26	31-Mar-26A	20-Apr-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-102	PreQualifcation SubmittalforConcrete Blocks	1400	100%	100%	31-Mar-26	15-Apr-26	31-Mar-26A	15-Apr-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-102	PreQualifcation Appovalfor Concrete Blocks	5.00	100%	100%	15-Apr-26	20-Apr-26	15-Apr-26A	20-Apr-26A	$000	$000	$0.00	0.00
WATERPROOFING		1200	0%	0%	31-Mar-26	13-Apr-26	31-Mar-26A	13-Apr-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-100	PreQualifcation SubmittalforWater Proding	1000	100%	100%	31-Mar-26	11-Apr-26	31-Mar-26A	11-Apr-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-101	PreQualifcation Appovalfor WaterProofing	3.00	100%	100%	11-Apr-26	13-Apr-26	11-Apr-26A	13-Apr-26A	$000	$000	$0.00	0.00
FLOORWALLTILES		1100	0%	0%	31-Mar-26	12-Apr-26	31-Mar-26A	12-Apr-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-102	PreQualifcation SubmittalforTiling Materials	1000	100%	100%	31-Mar-26	11-Apr-26	31-Mar-26A	11-Apr-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-102	PreQualifcation Appovalfor Tailling Material	2.00	100%	100%	11-Apr-26	12-Apr-26	11-Apr-26A	12-Apr-26A	$000	$000	$0.00	0.00
SUSPENDED CEILING		1200	0%	0%	31-Mar-26	13-Apr-26	31-Mar-26A	13-Apr-26A	$000	$000	$0.00	0.00
MLTX-02-004EN-102	PreQualifcation SubmittalforSuspendCeiling	1100	100%	100%	31-Mar-26	12-Apr-26	31-Mar-26A	12-Apr-26A	$000	$000	$0.00	0.00

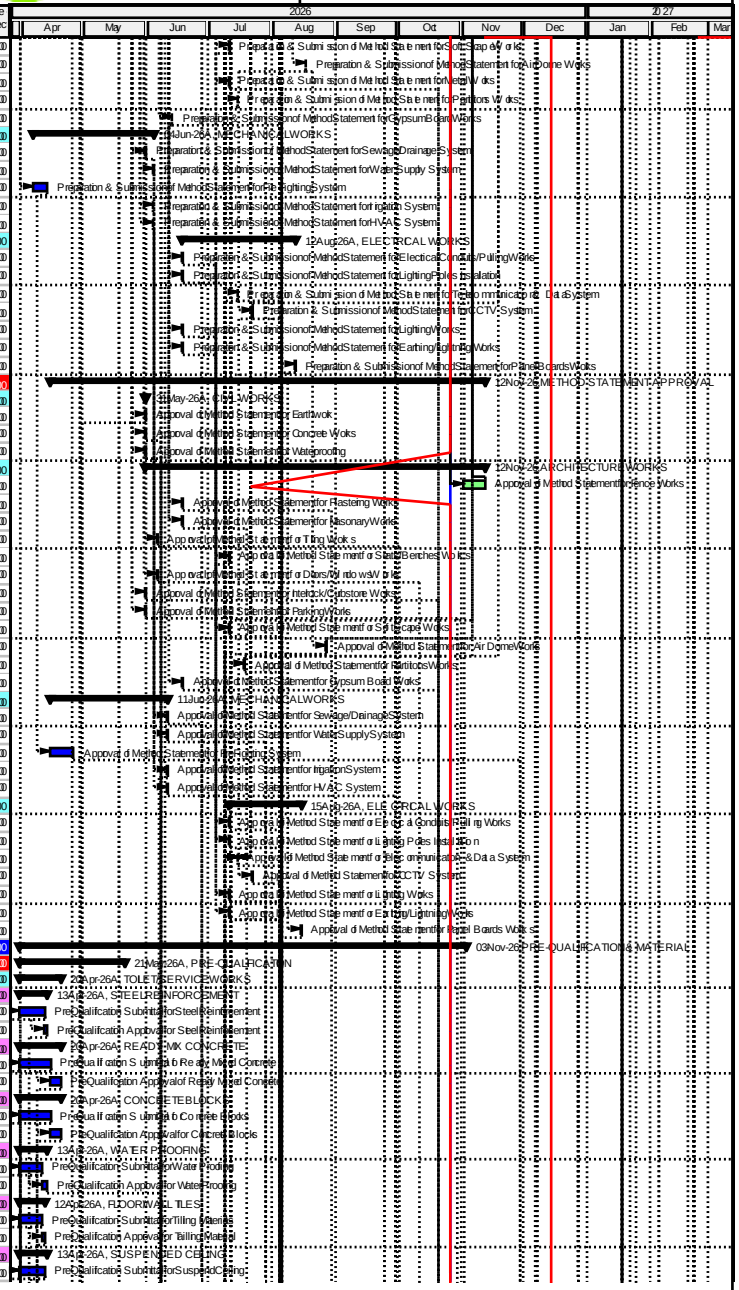


© Oracle Corporation

ActivityID	ActivityName	Orginal Duration	Schedule %	Performance% Complete	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Variance - BL Project
MLTX02-004EN-102	PreQualifcation Approval for Suspend Ceiling	2.00	100%	100%	12 Apr 26	13 Apr-26	12 Apr 26 A	13 Apr-26 A	$000	$000	$0.00	0.00
DOORS/WINDOWS		1100	0%	0%	31 Mar 26	12 Apr-26	31 Mar 26 A	12 Apr-26 A	$000	$000	$0.00	0.00
MLTX02-004EN-102	PreQualifcation Submittal for Doors/Windows	1000	100%	100%	31 Mar 26	11 Apr-26	31 Mar 26 A	11 Apr-26 A	$000	$000	$0.00	0.00
MLTX02-004EN-102	PreQualifcation Approval for Doors/Windows	2.00	100%	100%	11 Apr 26	12 Apr-26	11 Apr 26 A	12 Apr-26 A	$000	$000	$0.00	0.00
FURNITURES		1100	0%	0%	31 Mar 26	12 Apr-26	31 Mar 26 A	12 Apr-26 A	$000	$000	$0.00	0.00
MLTX02-004EN-103	PreQualifcation Submittal for Furnitures	1000	100%	100%	31 Mar 26	11 Apr-26	31 Mar 26 A	11 Apr-26 A	$000	$000	$0.00	0.00
MLTX02-004EN-104	PreQualifcation Approval for Furnitures	2.00	100%	100%	11 Apr 26	12 Apr-26	11 Apr 26 A	12 Apr-26 A	$000	$000	$0.00	0.00
SANITARY FIXTURES		1100	0%	0%	31 Mar 26	12 Apr-26	31 Mar 26 A	12 Apr-26 A	$000	$000	$0.00	0.00
MLTX02-004EN-102	PreQualifcation Submittal for Sanitary Fixtures	1000	100%	100%	31 Mar 26	11 Apr-26	31 Mar 26 A	11 Apr-26 A	$000	$000	$0.00	0.00
MLTX02-004EN-103	PreQualifcation Approval for Sanitary Fixtures	2.00	100%	100%	11 Apr 26	12 Apr-26	11 Apr 26 A	12 Apr-26 A	$000	$000	$0.00	0.00
WATER SUPPLY PIPES		1100	0%	0%	31 Mar 26	12 Apr-26	31 Mar 26 A	12 Apr-26 A	$000	$000	$0.00	0.00
MLTX02-004EN-103	PreQualifcation Submittal for Water Supply Pipes	1000	100%	100%	31 Mar 26	11 Apr-26	31 Mar 26 A	11 Apr-26 A	$000	$000	$0.00	0.00
MLTX02-004EN-103	PreQualifcation Approval for Water Supply Pipes	2.00	100%	100%	11 Apr 26	12 Apr-26	11 Apr 26 A	12 Apr-26 A	$000	$000	$0.00	0.00
SEWAGE DRAINAGE PIPES		1100	0%	0%	31 Mar 26	12 Apr-26	31 Mar 26 A	12 Apr-26 A	$000	$000	$0.00	0.00
MLTX02-004EN-103	PreQualifcation Submittal for Sewage Drainage Pipes	1000	100%	100%	31 Mar 26	11 Apr-26	31 Mar 26 A	11 Apr-26 A	$000	$000	$0.00	0.00
MLTX02-004EN-103	PreQualifcation Approval for Sewage/Drainage Pipes	2.00	100%	100%	11 Apr 26	12 Apr-26	11 Apr 26 A	12 Apr-26 A	$000	$000	$0.00	0.00
PACKAGE ACUNITS		8.00	0%	0%	07 Apr 26	15 Apr-26	07 Apr 26 A	15 Apr-26 A	$000	$000	$0.00	0.00
MLTX02-004EN-104	PreQualifcation Submittal for Package AC Units	6.00	100%	100%	07 Apr 26	13 Apr-26	07 Apr 26 A	13 Apr-26 A	$000	$000	$0.00	0.00
MLTX02-004EN-104	PreQualifcation Approval for Package AC Units	5.00	100%	100%	11 Apr 26	15 Apr-26	11 Apr 26 A	15 Apr-26 A	$000	$000	$0.00	0.00
AIRDFUSSERS/GRILLS		8.00	0%	0%	07 Apr 26	15 Apr-26	07 Apr 26 A	15 Apr-26 A	$000	$000	$0.00	0.00
MLTX02-004EN-104	PreQualifcation Submittal for Air Diffusers/Grills	6.00	100%	100%	07 Apr 26	13 Apr-26	07 Apr 26 A	13 Apr-26 A	$000	$000	$0.00	0.00
MLTX02-004EN-104	PreQualifcation Approval for Air Diffuses/Grills	5.00	100%	100%	11 Apr 26	15 Apr-26	11 Apr 26 A	15 Apr-26 A	$000	$000	$0.00	0.00
GALVANIZED DUCTS		8.00	0%	0%	07 Apr 26	15 Apr-26	07 Apr 26 A	15 Apr-26 A	$000	$000	$0.00	0.00
MLTX02-004EN-104	PreQualifcation Submittal for Galvarized Ducts	6.00	100%	100%	07 Apr 26	13 Apr-26	07 Apr 26 A	13 Apr-26 A	$000	$000	$0.00	0.00
MLTX02-004EN-104	PreQualifcation Approval for Galvanized Ducts	5.00	100%	100%	11 Apr 26	15 Apr-26	11 Apr 26 A	15 Apr-26 A	$000	$000	$0.00	0.00
EXHAUST FANS		8.00	0%	0%	07 Apr 26	15 Apr-26	07 Apr 26 A	15 Apr-26 A	$000	$000	$0.00	0.00
MLTX02-004EN-104	PreQualifcation Submittal for Exhaust Fans	5.00	100%	100%	07 Apr 26	12 Apr-26	07 Apr 26 A	12 Apr-26 A	$000	$000	$0.00	0.00
MLTX02-004EN-104	PreQualifcation Approval for Exhaust Fans	5.00	100%	100%	11 Apr 26	15 Apr-26	11 Apr 26 A	15 Apr-26 A	$000	$000	$0.00	0.00
LIGHTING FIXTURES		8.00	0%	0%	07 Apr 26	15 Apr-26	07 Apr 26 A	15 Apr-26 A	$000	$000	$0.00	0.00
MLTX02-004EN-103	PreQualifcation Submittal for Lighting Fixtures	3.00	100%	100%	07 Apr 26	09 Apr-26	07 Apr 26 A	09 Apr-26 A	$000	$000	$0.00	0.00
MLTX02-004EN-103	PreQualifcation Approval for Lighting Fixtures	5.00	100%	100%	11 Apr 26	15 Apr-26	11 Apr 26 A	15 Apr-26 A	$000	$000	$0.00	0.00
SWITCHES/SOCKETS		8.00	0%	0%	07 Apr 26	15 Apr-26	07 Apr 26 A	15 Apr-26 A	$000	$000	$0.00	0.00
MLTX02-004EN-103	PreQualifcation Submittal for Switches/Sockets	3.00	100%	100%	07 Apr 26	09 Apr-26	07 Apr 26 A	09 Apr-26 A	$000	$000	$0.00	0.00
MLTX02-004EN-103	PreQualifcation Approval for Switches/Sockets	5.00	100%	100%	11 Apr 26	15 Apr-26	11 Apr 26 A	15 Apr-26 A	$000	$000	$0.00	0.00
EARTHINGSYSTEM		8.00	0%	0%	07 Apr 26	15 Apr-26	07 Apr 26 A	15 Apr-26 A	$000	$000	$0.00	0.00
MLTX02-004EN-101	PreQualifcation Submittal for Earthing System	3.00	100%	100%	07 Apr 26	09 Apr-26	07 Apr 26 A	09 Apr-26 A	$000	$000	$0.00	0.00
MLTX02-004EN-101	PreQualifcation Approval for Eathing System	5.00	100%	100%	11 Apr 26	15 Apr-26	11 Apr 26 A	15 Apr-26 A	$000	$000	$0.00	0.00
DISTRBUTION PANNELS		8.00	0%	0%	07 Apr 26	15 Apr-26	07 Apr 26 A	15 Apr-26 A	$000	$000	$0.00	0.00
MLTX02-004EN-101	PreQualifcation Submittal for Distribution Panels	3.00	100%	100%	07 Apr 26	09 Apr-26	07 Apr 26 A	09 Apr-26 A	$000	$000	$0.00	0.00
MLTX02-004EN-102	PreQualifcation Approval for Distribution Panels	5.00	100%	100%	11 Apr 26	15 Apr-26	11 Apr 26 A	15 Apr-26 A	$000	$000	$0.00	0.00
PLAYGROUND WORKS		1800	0%	0%	31 Mar 26	20 Apr-26	31 Mar 26 A	20 Apr-26 A	$000	$000	$0.00	0.00
PVC MEMBRANE		1400	0%	0%	31 Mar 26	15 Apr-26	31 Mar 26 A	15 Apr-26 A	$000	$000	$0.00	0.00
MLTX02-004EN-105	PreQualifcation Submittal for PVC Membane	1200	100%	100%	31 Mar 26	13 Apr-26	31 Mar 26 A	13 Apr-26 A	$000	$000	$0.00	0.00
MLTX02-004EN-105	PreQualifcation Approval for PVC Membrane	3.00	100%	100%	13 Apr 26	15 Apr-26	13 Apr 26 A	15 Apr-26 A	$000	$000	$0.00	0.00
STEEL TENSION CABLES		1400	0%	0%	31 Mar 26	15 Apr-26	31 Mar 26 A	15 Apr-26 A	$000	$000	$0.00	0.00
MLTX02-004EN-106	PreQualifcation Submittal for Steel Tension Cables	1200	100%	100%	31 Mar 26	13 Apr-26	31 Mar 26 A	13 Apr-26 A	$000	$000	$0.00	0.00
MLTX02-004EN-106	PreQualifcation Approval for Steel Tension Cables	3.00	100%	100%	13 Apr 26	15 Apr-26	13 Apr 26 A	15 Apr-26 A	$000	$000	$0.00	0.00
EMERGENCY DOORS		1400	0%	0%	31 Mar 26	15 Apr-26	31 Mar 26 A	15 Apr-26 A	$000	$000	$0.00	0.00
MLTX02-004EN-106	PreQualifcation Submittal for Emergency Doos	1200	100%	100%	31 Mar 26	13 Apr-26	31 Mar 26 A	13 Apr-26 A	$000	$000	$0.00	0.00
MLTX02-004EN-106	PreQualifcation Approval for Emergency Doors	3.00	100%	100%	13 Apr 26	15 Apr-26	13 Apr 26 A	15 Apr-26 A	$000	$000	$0.00	0.00
PRESSURE UNITS		1400	0%	0%	31 Mar 26	15 Apr-26	31 Mar 26 A	15 Apr-26 A	$000	$000	$0.00	0.00
MLTX02-004EN-106	PreQualifcation Submittal for Pressue Units	1200	100%	100%	31 Mar 26	13 Apr-26	31 Mar 26 A	13 Apr-26 A	$000	$000	$0.00	0.00
MLTX02-004EN-106	PreQualifcation Approval for Pessue Units	3.00	100%	100%	13 Apr 26	15 Apr-26	13 Apr 26 A	15 Apr-26 A	$000	$000	$0.00	0.00
AIRLOCK DOORS		1400	0%	0%	31 Mar 26	15 Apr-26	31 Mar 26 A	15 Apr-26 A	$000	$000	$0.00	0.00
MLTX02-004EN-106	PreQualifcation Submittal for Lock Doors	1200	100%	100%	31 Mar 26	13 Apr-26	31 Mar 26 A	13 Apr-26 A	$000	$000	$0.00	0.00
MLTX02-004EN-106	PreQualifcation Approval for lock Doos	3.00	100%	100%	13 Apr 26	15 Apr-26	13 Apr 26 A	15 Apr-26 A	$000	$000	$0.00	0.00
ARTIFICIAL TURF		1100	0%	0%	31 Mar 26	12 Apr-26	31 Mar 26 A	12 Apr-26 A	$000	$000	$0.00	0.00
MLTX02-004EN-107	PreQualifcation Submittal for Artificial TURF	1000	100%	100%	31 Mar 26	11 Apr-26	31 Mar 26 A	11 Apr-26 A	$000	$000	$0.00	0.00
MLTX02-004EN-105	PreQualifcation Approval for Artificial TURF	2.00	100%	100%	11 Apr 26	12 Apr-26	11 Apr 26 A	12 Apr-26 A	$000	$000	$0.00	0.00
RUBBER GRANULES		1400	0%	0%	31 Mar 26	15 Apr-26	31 Mar 26 A	15 Apr-26 A	$000	$000	$0.00	0.00
MLTX02-004EN-107	PreQualifcation Submittal for Rubber Granules	1200	100%	100%	31 Mar 26	13 Apr-26	31 Mar 26 A	13 Apr-26 A	$000	$000	$0.00	0.00
MLTX02-004EN-105	PreQualifcation Approval for Rubber Granules	3.00	100%	100%	13 Apr 26	15 Apr-26	13 Apr 26 A	15 Apr-26 A	$000	$000	$0.00	0.00
PADEL GLASS		1400	0%	0%	31 Mar 26	15 Apr-26	31 Mar 26 A	15 Apr-26 A	$000	$000	$0.00	0.00
MLTX02-004EN-106	PreQualifcation Submittal for Padel Glass	1200	100%	100%	31 Mar 26	13 Apr-26	31 Mar 26 A	13 Apr-26 A	$000	$000	$0.00	0.00
MLTX02-004EN-106	PreQualifcation Approval for Padel Glass	3.00	100%	100%	13 Apr 26	15 Apr-26	13 Apr 26 A	15 Apr-26 A	$000	$000	$0.00	0.00
PADEL WIRE MESH/STEEL SETS		1400	0%	0%	31 Mar 26	15 Apr-26	31 Mar 26 A	15 Apr-26 A	$000	$000	$0.00	0.00
MLTX02-004EN-106	PreQualifcation Submittal for Wire Mesh/Steel Sets	1200	100%	100%	31 Mar 26	13 Apr-26	31 Mar 26 A	13 Apr-26 A	$000	$000	$0.00	0.00
MLTX02-004EN-106	PreQualifcation Approval for Wire Mesh/Steel Sets	3.00	100%	100%	13 Apr 26	15 Apr-26	13 Apr 26 A	15 Apr-26 A	$000	$000	$0.00	0.00
AGGREGATE BASE COURSE		1800	0%	0%	31 Mar 26	20 Apr-26	31 Mar 26 A	20 Apr-26 A	$000	$000	$0.00	0.00
MLTX02-004EN-106	PreQualifcation Submittal for Aggregate Base Course	1800	100%	100%	31 Mar 26	20 Apr-26	31 Mar 26 A	20 Apr-26 A	$000	$000	$0.00	0.00
MLTX02-004EN-106	PreQualifcation Approval for Aggregate Base Course	3.00	100%	100%	18 Apr 26	20 Apr-26	18 Apr 26 A	20 Apr-26 A	$000	$000	$0.00	0.00
BITUMNOUS BASE & WEARING COURSE		7.00	0%	0%	07 Apr 26	14 Apr-26	07 Apr 26 A	14 Apr-26 A	$000	$000	$0.00	0.00

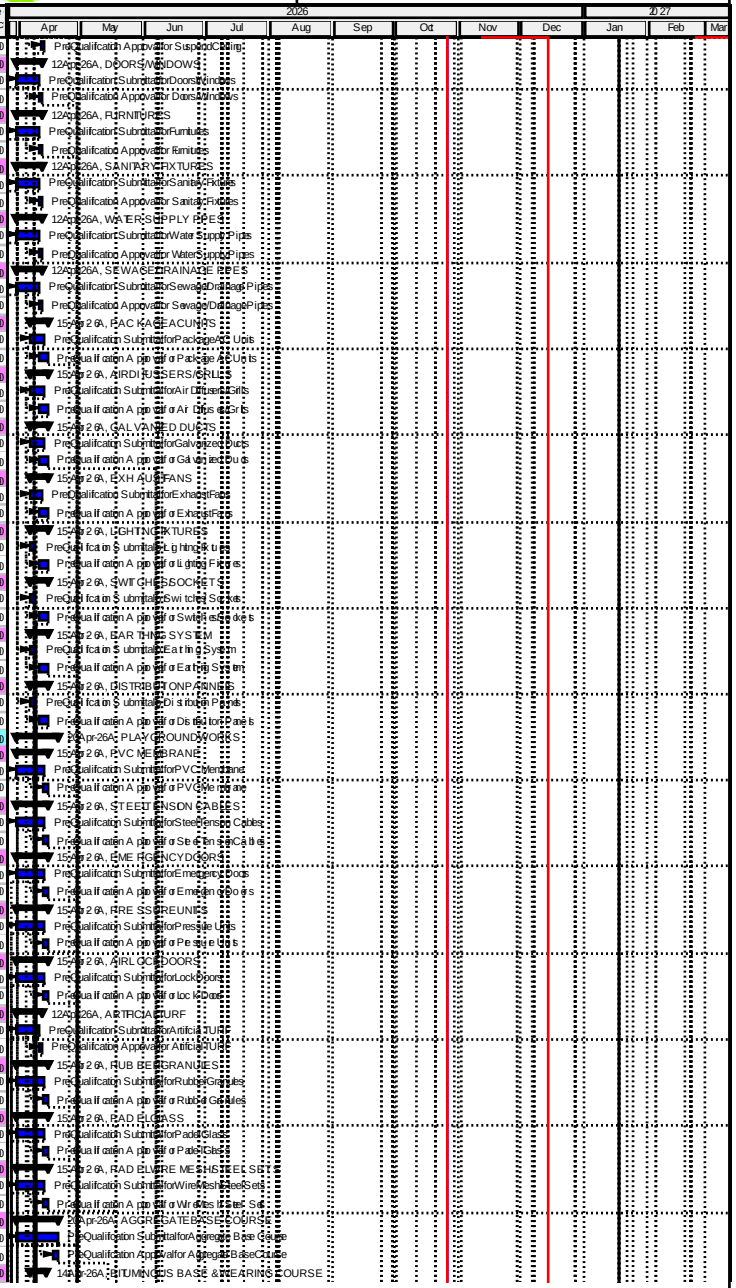


© Oracle Corporation

ActivityID	ActivityName	Orginal Duration	Schedule %	Performance% Complete	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Variance - BL Project
MLTX02-004EN-100	PreQualification SubmittalforBituminous Base & WearingCource	5.00	100%	100%	07-Apr-26	12-Apr-26	07-Apr-26A	12-Apr-26A	$000	$000	$0.00	0.00
MLTX02-004EN-100	PreQualification Approvalfor the Site	3.00	100%	100%	12-Apr-26	14-Apr-26	12-Apr-26A	14-Apr-26A	$000	$000	$0.00	0.00
INTERLOCKING PAVING		12.00	0%	0%	07-Apr-26	20-Apr-26	07-Apr-26A	20-Apr-26A	$000	$000	$0.00	0.00
MLTX02-004EN-100	PreQualification SubmittalforInterlocking Block Pavers	8.00	100%	100%	07-Apr-26	15-Apr-26	07-Apr-26A	15-Apr-26A	$000	$000	$0.00	0.00
MLTX02-004EN-101	PreQualification Approvalfor Interlocking BlockPavers	5.00	100%	100%	15-Apr-26	20-Apr-26	15-Apr-26A	20-Apr-26A	$000	$000	$0.00	0.00
MARKINGPAINT		8.00	0%	0%	04-Apr-26	12-Apr-26	04-Apr-26A	12-Apr-26A	$000	$000	$0.00	0.00
MLTX02-004EN-104	PreQualification SubmittalforMarking Paint	8.00	100%	100%	04-Apr-26	12-Apr-26	04-Apr-26A	12-Apr-26A	$000	$000	$0.00	0.00
MLTX02-004EN-105	PreQualification Approvalfor MakingPaint	1.00	100%	100%	12-Apr-26	12-Apr-26	12-Apr-26A	12-Apr-26A	$000	$000	$0.00	0.00
PACKAGE ACUNITS		11.00	0%	0%	04-Apr-26	15-Apr-26	04-Apr-26A	15-Apr-26A	$000	$000	$0.00	0.00
MLTX02-004EN-105	PreQualification SubmittalforPackageAC Units	9.00	100%	100%	04-Apr-26	13-Apr-26	04-Apr-26A	13-Apr-26A	$000	$000	$0.00	0.00
MLTX02-004EN-105	PreQualification Approvalfor PackageAC Units	3.00	100%	100%	13-Apr-26	15-Apr-26	13-Apr-26A	15-Apr-26A	$000	$000	$0.00	0.00
AIRDIFUSSERS/GRILLS		11.00	0%	0%	04-Apr-26	15-Apr-26	04-Apr-26A	15-Apr-26A	$000	$000	$0.00	0.00
MLTX02-004EN-105	PreQualification SubmittalforAir Difussers/Grills	9.00	100%	100%	04-Apr-26	13-Apr-26	04-Apr-26A	13-Apr-26A	$000	$000	$0.00	0.00
MLTX02-004EN-105	PreQualification Approvalfor Air Difussers/Grills	3.00	100%	100%	13-Apr-26	15-Apr-26	13-Apr-26A	15-Apr-26A	$000	$000	$0.00	0.00
GALVANIZEDD UCTS		11.00	0%	0%	04-Apr-26	15-Apr-26	04-Apr-26A	15-Apr-26A	$000	$000	$0.00	0.00
MLTX02-004EN-105	PreQualification SubmittalforGalvanized Duct	9.00	100%	100%	04-Apr-26	13-Apr-26	04-Apr-26A	13-Apr-26A	$000	$000	$0.00	0.00
MLTX02-004EN-105	PreQualification Approvalfor Galvanized Duct	3.00	100%	100%	13-Apr-26	15-Apr-26	13-Apr-26A	15-Apr-26A	$000	$000	$0.00	0.00
EXHAUSTFANS		11.00	0%	0%	04-Apr-26	15-Apr-26	04-Apr-26A	15-Apr-26A	$000	$000	$0.00	0.00
MLTX02-004EN-105	PreQualification SubmittalforExhaustFans	9.00	100%	100%	04-Apr-26	13-Apr-26	04-Apr-26A	13-Apr-26A	$000	$000	$0.00	0.00
MLTX02-004EN-105	PreQualification Approvalfor ExhaustFans	3.00	100%	100%	13-Apr-26	15-Apr-26	13-Apr-26A	15-Apr-26A	$000	$000	$0.00	0.00
DISTRBUTON BOARDS		11.00	0%	0%	04-Apr-26	15-Apr-26	04-Apr-26A	15-Apr-26A	$000	$000	$0.00	0.00
MLTX02-004EN-106	PreQualification SubmittalforDistibution Boards	9.00	100%	100%	04-Apr-26	13-Apr-26	04-Apr-26A	13-Apr-26A	$000	$000	$0.00	0.00
MLTX02-004EN-106	PreQualification Approvalfor Distribution Boards	3.00	100%	100%	13-Apr-26	15-Apr-26	13-Apr-26A	15-Apr-26A	$000	$000	$0.00	0.00
POWERCABLES		11.00	0%	0%	04-Apr-26	15-Apr-26	04-Apr-26A	15-Apr-26A	$000	$000	$0.00	0.00
MLTX02-004EN-106	PreQualification SubmittalforPowerCables	9.00	100%	100%	04-Apr-26	13-Apr-26	04-Apr-26A	13-Apr-26A	$000	$000	$0.00	0.00
MLTX02-004EN-106	PreQualification Approvalfor Power Cables	3.00	100%	100%	13-Apr-26	15-Apr-26	13-Apr-26A	15-Apr-26A	$000	$000	$0.00	0.00
LIGHTFXTURES		11.00	0%	0%	04-Apr-26	15-Apr-26	04-Apr-26A	15-Apr-26A	$000	$000	$0.00	0.00
MLTX02-004EN-106	PreQualification SubmittalforLightFixtures	9.00	100%	100%	04-Apr-26	13-Apr-26	04-Apr-26A	13-Apr-26A	$000	$000	$0.00	0.00
MLTX02-004EN-106	PreQualification Approvalfor LightFixtures	3.00	100%	100%	13-Apr-26	15-Apr-26	13-Apr-26A	15-Apr-26A	$000	$000	$0.00	0.00
CCTV MATERIALS		11.00	0%	0%	04-Apr-26	15-Apr-26	04-Apr-26A	15-Apr-26A	$000	$000	$0.00	0.00
MLTX02-004EN-107	PreQualification SubmittalforCCTV	9.00	100%	100%	04-Apr-26	13-Apr-26	04-Apr-26A	13-Apr-26A	$000	$000	$0.00	0.00
MLTX02-004EN-107	PreQualification Approvalfor CCTV	3.00	100%	100%	13-Apr-26	15-Apr-26	13-Apr-26A	15-Apr-26A	$000	$000	$0.00	0.00
POWEROUTLETS/SWITCHES		11.00	0%	0%	04-Apr-26	15-Apr-26	04-Apr-26A	15-Apr-26A	$000	$000	$0.00	0.00
MLTX02-004EN-107	PreQualification SubmittalforPowerOutlets/Switches	9.00	100%	100%	04-Apr-26	13-Apr-26	04-Apr-26A	13-Apr-26A	$000	$000	$0.00	0.00
MLTX02-004EN-107	PreQualification Approvalfor Power OutletsSwitches	3.00	100%	100%	13-Apr-26	15-Apr-26	13-Apr-26A	15-Apr-26A	$000	$000	$0.00	0.00
LANDSCAPE WORKS		42.00	0%	0%	04-Apr-26	21-May-26	04-Apr-26A	21-May-26A	$000	$000	$0.00	0.00
INTERLOCKING PAVING		15.00	0%	0%	04-Apr-26	20-Apr-26	04-Apr-26A	20-Apr-26A	$000	$000	$0.00	0.00
MLTX02-004EN-107	PreQualification SubmittalforInterlocking Block Pavers	11.00	100%	100%	04-Apr-26	15-Apr-26	04-Apr-26A	15-Apr-26A	$000	$000	$0.00	0.00
MLTX02-004EN-107	PreQualification Approvalfor Interlocking BlockPavers	5.00	100%	100%	15-Apr-26	20-Apr-26	15-Apr-26A	20-Apr-26A	$000	$000	$0.00	0.00
CURBSTONE		15.00	0%	0%	04-Apr-26	20-Apr-26	04-Apr-26A	20-Apr-26A	$000	$000	$0.00	0.00
MLTX02-004EN-108	PreQualification SubmittalforCurbstone	11.00	100%	100%	04-Apr-26	15-Apr-26	04-Apr-26A	15-Apr-26A	$000	$000	$0.00	0.00
MLTX02-004EN-108	PreQualification Approvalfor Cubstone	5.00	100%	100%	15-Apr-26	20-Apr-26	15-Apr-26A	20-Apr-26A	$000	$000	$0.00	0.00
PAVEMENTMARKNG		8.00	0%	0%	04-Apr-26	12-Apr-26	04-Apr-26A	12-Apr-26A	$000	$000	$0.00	0.00
MLTX02-004EN-100	PreQualification SubmittalforPavementMarkings	3.00	100%	100%	04-Apr-26	06-Apr-26	04-Apr-26A	06-Apr-26A	$000	$000	$0.00	0.00
MLTX02-004EN-101	PreQualification Approvalfor PavementMarkings	5.00	100%	100%	07-Apr-26	12-Apr-26	07-Apr-26A	12-Apr-26A	$000	$000	$0.00	0.00
TRAFFC SIGNS		14.00	0%	0%	06-May-26	21-May-26	06-May-26A	21-May-26A	$000	$000	$0.00	0.00
MLTX02-004EN-100	PreQualification SubmittalforTraffic Signs	1.00	100%	100%	06-May-26	06-May-26	06-May-26A	06-May-26A	$000	$000	$0.00	0.00
MLTX02-004EN-101	PreQualification Approvalfor Traffic Signs	1.00	100%	100%	21-May-26	21-May-26	21-May-26A	21-May-26A	$000	$000	$0.00	0.00
IRRGATIONPI PESSPRINKLERS		42.00	0%	0%	04-Apr-26	21-May-26	04-Apr-26A	21-May-26A	$000	$000	$0.00	0.00
MLTX02-004EN-101	PreQualification SubmittalforIrrigation Pipes/Sprinkles	20.00	100%	100%	04-Apr-26	26-Apr-26	04-Apr-26A	26-Apr-26A	$000	$000	$0.00	0.00
MLTX02-004EN-101	PreQualification Approvalfor IrrigationPipesSprinkles	1.00	100%	100%	21-May-26	21-May-26	21-May-26A	21-May-26A	$000	$000	$0.00	0.00
AGRICULTURE SOIL		42.00	0%	0%	04-Apr-26	21-May-26	04-Apr-26A	21-May-26A	$000	$000	$0.00	0.00
MLTX02-004EN-108	PreQualification SubmittalforAgricultue Soil	20.00	100%	100%	04-Apr-26	26-Apr-26	04-Apr-26A	26-Apr-26A	$000	$000	$0.00	0.00
MLTX02-004EN-108	PreQualification Approvalfor AgricutureSoil	1.00	100%	100%	21-May-26	21-May-26	21-May-26A	21-May-26A	$000	$000	$0.00	0.00
TRACK SURFACE		8.00	0%	0%	04-Apr-26	12-Apr-26	04-Apr-26A	12-Apr-26A	$000	$000	$0.00	0.00
MLTX02-004EN-108	PreQualification SubmittalforTrackSurface	3.00	100%	100%	04-Apr-26	06-Apr-26	04-Apr-26A	06-Apr-26A	$000	$000	$0.00	0.00
MLTX02-004EN-108	PreQualification Approvalfor TrackSurface	5.00	100%	100%	07-Apr-26	12-Apr-26	07-Apr-26A	12-Apr-26A	$000	$000	$0.00	0.00
GRASS/TREES		14.00	0%	0%	04-Apr-26	19-Apr-26	04-Apr-26A	19-Apr-26A	$000	$000	$0.00	0.00
MLTX02-004EN-108	PreQualification SubmittalforGrass/Trees	10.00	100%	100%	04-Apr-26	14-Apr-26	04-Apr-26A	14-Apr-26A	$000	$000	$0.00	0.00
MLTX02-004EN-108	PreQualification Approvalfor Gass/Tees	5.00	100%	100%	14-Apr-26	19-Apr-26	14-Apr-26A	19-Apr-26A	$000	$000	$0.00	0.00
CABIES		2.00	0%	0%	06-May-26	07-May-26	06-May-26A	07-May-26A	$000	$000	$0.00	0.00
MLTX02-004EN-107	PreQualification SubmittalforCables	1.00	100%	100%	06-May-26	06-May-26	06-May-26A	06-May-26A	$000	$000	$0.00	0.00
MLTX02-004EN-107	PreQualification Approvalfor Cables	1.00	100%	100%	07-May-26	07-May-26	07-May-26A	07-May-26A	$000	$000	$0.00	0.00
LIGHTPOLES		2.00	0%	0%	06-May-26	07-May-26	06-May-26A	07-May-26A	$000	$000	$0.00	0.00
MLTX02-004EN-997	PreQualification SubmittalforLighting poles	1.00	100%	100%	06-May-26	06-May-26	06-May-26A	06-May-26A	$000	$000	$0.00	0.00
MLTX02-004EN-998	PreQualification Approvalfor Lighting poles	1.00	100%	100%	07-May-26	07-May-26	07-May-26A	07-May-26A	$000	$000	$0.00	0.00
MATERIALSUBMITTAL		177.00	0%	0%	07-Apr-26	18-Jul-26	07-Apr-26A	03-Nov-26	$000	$000	$0.00	-92.00
TOILETSERVICEWORKS		164.00	0%	0%	11-Apr-26	12-Jul-26	11-Apr-26A	22-Jul-26A	$000	$000	$0.00	-9.00
STEELREINFORCEMENT		2.00	0%	0%	11-Apr-26	12-Apr-26	11-Apr-26A	12-Apr-26A	$000	$000	$0.00	0.00
MLTX02-004EN-899	MaterialSubmittal for Steel Reinforement	1.00	100%	100%	11-Apr-26	11-Apr-26	11-Apr-26A	11-Apr-26A	$000	$000	$0.00	0.00
MLTX02-004EN-910	MaterialApprovalforSteelReinbrcement	2.00	100%	100%	11-Apr-26	12-Apr-26	11-Apr-26A	12-Apr-26A	$000	$000	$0.00	0.00
READY MKCONCRETE		10.00	0%	0%	15-Apr-26	26-Apr-26	15-Apr-26A	26-Apr-26A	$000	$000	$0.00	0.00
MLTX02-004EN-900	MaterialSubmittal for Ready MixedConcete	3.00	100%	100%	15-Apr-26	18-Apr-26	15-Apr-26A	18-Apr-26A	$000	$000	$0.00	0.00

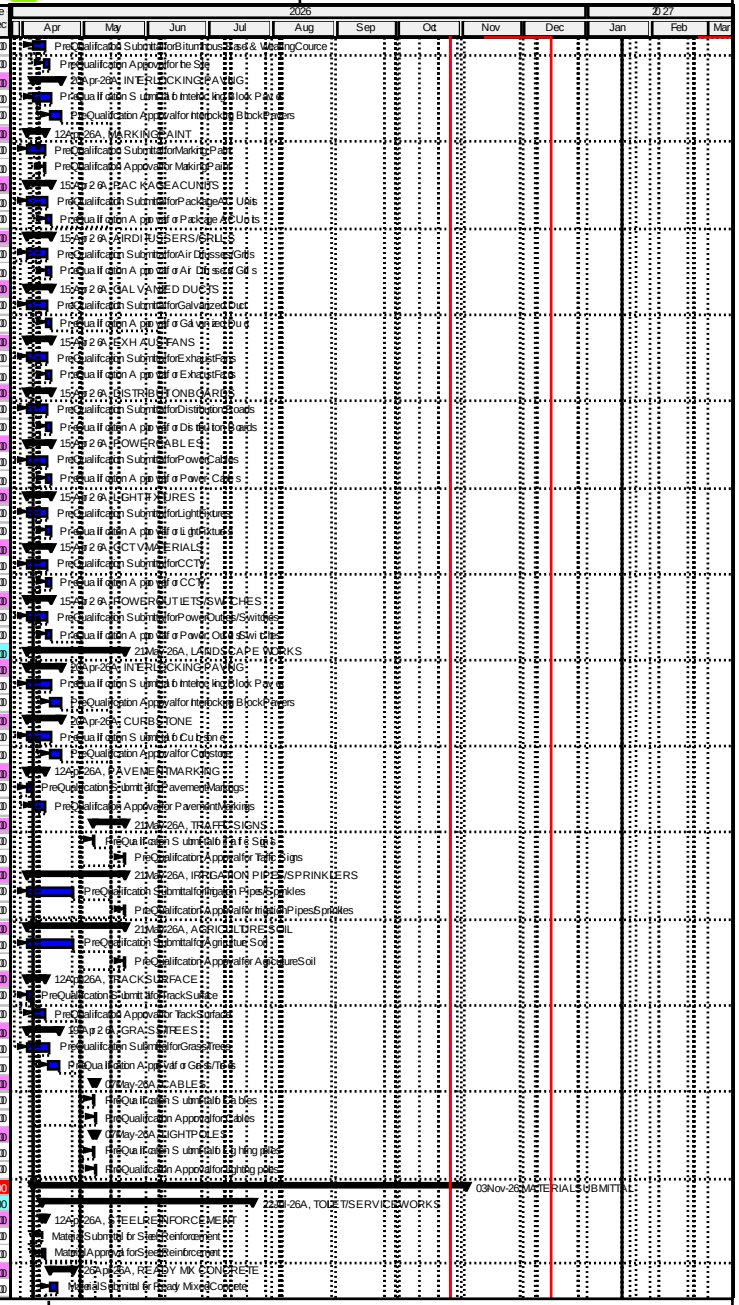


© Oracle Corporation

ActivityID	ActivityName	Orginal Duration	Schedule %	Performance% Complete	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cos	Earned Value Cos	Budgeted Tot Cos	Variance - BL Project
MLTX02-004EN-901	Material Approval of Ready Mixed Concrete	7.0	100%	100%	19 Apr 26	26Apr-26	19 Apr 26 A	26Apr-26A	$000	$000	$0.0	0.0
CONCRETE BLOCKS		1000	0%	0%	15 Apr 26	26Apr-26	15 Apr 26 A	26Apr-26A	$000	$000	$0.0	0.0
MLTX02-004EN-915	Material Submittal for Concrete Blocks	3.0	100%	100%	15 Apr 26	18Apr-26	15 Apr 26 A	18Apr-26A	$000	$000	$0.0	0.0
MLTX02-004EN-924	Material Approval for Concrete Blocks	7.0	100%	100%	19 Apr 26	26Apr-26	19 Apr 26 A	26Apr-26A	$000	$000	$0.0	0.0
FLOORINALL TILES		8800	0%	0%	15 Apr 26	12Jul-26	15 Apr 26 A	22Jul-26A	$000	$000	$0.0	-900
MLTX02-004EN-921	Material Submittal for TilingMaterials	3.0	100%	100%	15 Apr 26	18Apr-26	15 Apr 26 A	18Apr-26A	$000	$000	$0.0	0.0
MLTX02-004EN-922	Material Approval for TilingMaterial	7.0	100%	100%	05 Jul-26	12Jul-26	22 Jul-26A	22Jul-26A	$000	$000	$0.0	6.0
SUSPENDED CEILING		5.0	0%	0%	15 Apr 26	20Apr-26	15 Apr 26 A	20Apr-26A	$000	$000	$0.0	0.0
MLTX02-004EN-922	Material Submittal for Suspend Ceiling	3.0	100%	100%	15 Apr 26	18Apr-26	15 Apr 26 A	18Apr-26A	$000	$000	$0.0	0.0
MLTX02-004EN-924	Material Approval for Suspend Ceiling	2.0	100%	100%	19 Apr 26	20Apr-26	19 Apr 26 A	20Apr-26A	$000	$000	$0.0	0.0
DOORS/WINDOWS		1400	0%	0%	06 May-26	21May-26	06 May 26 A	21May-26A	$000	$000	$0.0	0.0
MLTX02-004EN-925	Material Submittal for Doos/Windows	1.0	100%	100%	06 May-26	06May-26	06 May 26 A	06May-26A	$000	$000	$0.0	0.0
MLTX02-004EN-926	Material Approval for Doors/Windows	1.0	100%	100%	21 May-26	21May-26	21 May 26 A	21May-26A	$000	$000	$0.0	0.0
FURNITURES		2.0	0%	0%	06 May-26	07May-26	06 May 26 A	07May-26A	$000	$000	$0.0	0.0
MLTX02-004EN-937	Material Submittal for Furnitures	1.0	100%	100%	06 May-26	06May-26	06 May 26 A	06May-26A	$000	$000	$0.0	0.0
MLTX02-004EN-938	Material Approval for Furnitures	1.0	100%	100%	07 May-26	07May-26	07 May 26 A	07May-26A	$000	$000	$0.0	0.0
SANITARYFIXTURES		1400	0%	0%	15 Apr 26	30Apr-26	15 Apr 26 A	30Apr-26A	$000	$000	$0.0	0.0
MLTX02-004EN-927	Material Submittal for SanitaryFixtures	6.0	100%	100%	15 Apr 26	21Apr-26	15 Apr 26 A	21Apr-26A	$000	$000	$0.0	0.0
MLTX02-004EN-928	Material Approval for Sanitary fixtures	1100	100%	100%	19 Apr 26	30Apr-26	19 Apr 26 A	30Apr-26A	$000	$000	$0.0	0.0
WATERSUPPLY PIPES		2.0	0%	0%	15 Apr 26	16Apr-26	15 Apr 26 A	16Apr-26A	$000	$000	$0.0	0.0
MLTX02-004EN-929	Material Submittal for Water Supply Pipes	1.0	100%	100%	15 Apr 26	15Apr-26	15 Apr 26 A	15Apr-26A	$000	$000	$0.0	0.0
MLTX02-004EN-930	Material Approval for Water Supply Pipes	2.0	100%	100%	15 Apr 26	16Apr-26	15 Apr 26 A	16Apr-26A	$000	$000	$0.0	0.0
SEWAGEDRAINAGEPIPES		2.0	0%	0%	15 Apr 26	16Apr-26	15 Apr 26 A	16Apr-26A	$000	$000	$0.0	0.0
MLTX02-004EN-931	Material Submittal for Sewage/Drainage Pipes	1.0	100%	100%	15 Apr 26	15Apr-26	15 Apr 26 A	15Apr-26A	$000	$000	$0.0	0.0
MLTX02-004EN-932	Material Approval for SewageDrainage Pipes	2.0	100%	100%	15 Apr 26	16Apr-26	15 Apr 26 A	16Apr-26A	$000	$000	$0.0	0.0
PACKAGE ACUNITS		2.0	0%	0%	06 May-26	07May-26	06 May 26 A	07May-26A	$000	$000	$0.0	0.0
MLTX02-004EN-940	Material Submittal for Package ACUnits	1.0	100%	100%	06 May-26	06May-26	06 May 26 A	06May-26A	$000	$000	$0.0	0.0
MLTX02-004EN-941	Material Approval for Package AC Units	1.0	100%	100%	07 May-26	07May-26	07 May 26 A	07May-26A	$000	$000	$0.0	0.0
AIRDFUSSERS/GRILLS		1800	0%	0%	16 Apr 26	06May-26	16 Apr 26 A	06May-26A	$000	$000	$0.0	0.0
MLTX02-004EN-942	Material Submittal for AirDiffusersGrills	6.0	100%	100%	16 Apr 26	22Apr-26	16 Apr 26 A	22Apr-26A	$000	$000	$0.0	0.0
MLTX02-004EN-943	Material Approval for AirDiffusers/Grills	1.0	100%	100%	06 May-26	06May-26	06 May 26 A	06May-26A	$000	$000	$0.0	0.0
GALVANIZEDDUCTS		11300	0%	0%	13 Jun 26	11Jul-26	13 Jun 26 A	17Jun-26A	$000	$000	$0.0	20.0
MLTX02-004EN-944	Material Submittal for GalvanizedDucts	1.0	100%	100%	13 Jun 26	13Jun-26	13 Jun 26 A	13Jun-26A	$000	$000	$0.0	0.0
MLTX02-004EN-945	Material Approval for GalvanizedDucts	6.0	100%	100%	05 Jul-26	11Jul-26	17 Jun 26 A	17Jun-26A	$000	$000	$0.0	5.0
EXHAUSTFANS		1800	0%	0%	16 Apr 26	06May-26	16 Apr 26 A	06May-26A	$000	$000	$0.0	0.0
MLTX02-004EN-946	Material Submittal for Exhaust Fans	2.0	100%	100%	16 Apr 26	18Apr-26	16 Apr 26 A	18Apr-26A	$000	$000	$0.0	0.0
MLTX02-004EN-947	Material Approval for Exhaust Fans	1.0	100%	100%	06 May-26	06May-26	06 May 26 A	06May-26A	$000	$000	$0.0	0.0
LIGHTING FIXTURES		8.0	0%	0%	16 Apr 26	25Apr-26	16 Apr 26 A	25Apr-26A	$000	$000	$0.0	0.0
MLTX02-004EN-933	Material Submittal for LightingFixtures	3.0	100%	100%	16 Apr 26	19Apr-26	16 Apr 26 A	19Apr-26A	$000	$000	$0.0	0.0
MLTX02-004EN-934	Material Approval for LightingFixtues	5.0	100%	100%	20 Apr 26	25Apr-26	20 Apr 26 A	25Apr-26A	$000	$000	$0.0	0.0
SWITCHES/SOCKETS		8.0	0%	0%	16 Apr 26	25Apr-26	16 Apr 26 A	25Apr-26A	$000	$000	$0.0	0.0
MLTX02-004EN-935	Material Submittal for Switches/Sockets	3.0	100%	100%	16 Apr 26	19Apr-26	16 Apr 26 A	19Apr-26A	$000	$000	$0.0	0.0
MLTX02-004EN-936	Material Approval for Switches/Sockets	5.0	100%	100%	20 Apr 26	25Apr-26	20 Apr 26 A	25Apr-26A	$000	$000	$0.0	0.0
EARTHINGSYSTEM		2.0	0%	0%	06 May-26	07May-26	06 May 26 A	07May-26A	$000	$000	$0.0	0.0
MLTX02-004EN-915	Material Submittal for EarthingSystem	1.0	100%	100%	06 May-26	06May-26	06 May 26 A	06May-26A	$000	$000	$0.0	0.0
MLTX02-004EN-916	Material Approval for Earthing System	1.0	100%	100%	07 May-26	07May-26	07 May 26 A	07May-26A	$000	$000	$0.0	0.0
DISTRBUTON PANNELS		8.0	0%	0%	16 Apr 26	25Apr-26	16 Apr 26 A	25Apr-26A	$000	$000	$0.0	0.0
MLTX02-004EN-917	Material Submittal for DistributionPanels	3.0	100%	100%	16 Apr 26	19Apr-26	16 Apr 26 A	19Apr-26A	$000	$000	$0.0	0.0
MLTX02-004EN-918	Material Approval for Distibuton Panels	5.0	100%	100%	20 Apr 26	25Apr-26	20 Apr 26 A	25Apr-26A	$000	$000	$0.0	0.0
PLAYGROUND WORKS		17300	0%	0%	12 Apr 26	12Jul-26	12 Apr 26 A	03Nov-26	$000	$000	$0.0	-9700
PVC MEMBRANE		15200	0%	0%	06 May-26	12Jul-26	06 May 26 A	03Nov-26	$000	$000	$0.0	-9700
MLTX02-004EN-957	Material Approval for PVC Membane	7.0	100%	0%	05 Jul-26	12Jul-26	27 Oct26	03Nov-26	$000	$000	$0.0	0.0
MLTX02-004EN-956	Material Submittal for PVC Membrane	1.0	100%	100%	06 May-26	06May-26	06 May 26 A	06May-26A	$000	$000	$0.0	0.0
STEELTENSION CABLES		15200	0%	0%	06 May-26	12Jul-26	06 May 26 A	03Nov-26	$000	$000	$0.0	-9700
MLTX02-004EN-988	Material Approval for Steel Tension Cables	7.0	100%	0%	05 Jul-26	12Jul-26	27 Oct26	03Nov-26	$000	$000	$0.0	0.0
MLTX02-004EN-958	Material Submittal for Steel TensionCables	1.0	100%	100%	06 May-26	06May-26	06 May 26 A	06May-26A	$000	$000	$0.0	0.0
EMERGENCY DOORS		15200	0%	0%	06 May-26	12Jul-26	06 May 26 A	03Nov-26	$000	$000	$0.0	-9700
MLTX02-004EN-988	Material Approval for Emergency Doos	7.0	100%	0%	05 Jul-26	12Jul-26	27 Oct26	03Nov-26	$000	$000	$0.0	0.0
MLTX02-004EN-955	Material Submittal for Emegency Doors	1.0	100%	100%	06 May-26	06May-26	06 May 26 A	06May-26A	$000	$000	$0.0	0.0
PRESSURE UNITS		14300	0%	0%	06 May-26	12Jul-26	06 May 26 A	24Aug-26A	$000	$000	$0.0	-3700
MLTX02-004EN-960	Material Submittal for PressureUnits	1.0	100%	100%	06 May-26	06May-26	06 May 26 A	06May-26A	$000	$000	$0.0	0.0
MLTX02-004EN-990	Material Approval for Pressure Units	7.0	100%	100%	05 Jul-26	12Jul-26	24 Aug 26 A	24Aug-26A	$000	$000	$0.0	6.0
AIRLOCK DOORS		15200	0%	0%	06 May-26	12Jul-26	06 May 26 A	03Nov-26	$000	$000	$0.0	-9700
MLTX02-004EN-991	Material Approval for LockDoors	7.0	100%	0%	05 Jul-26	12Jul-26	27 Oct26	03Nov-26	$000	$000	$0.0	0.0
MLTX02-004EN-961	Material Submittal for Lock Doors	5.0	100%	100%	06 May-26	11May-26	06 May 26 A	11May-26A	$000	$000	$0.0	0.0
ARTIFICIAL TURF		1700	0%	0%	12 Apr 26	30Apr-26	12 Apr 26 A	30Apr-26A	$000	$000	$0.0	0.0
MLTX02-004EN-976	Material Submittal for Artificial TURF	1500	100%	100%	12 Apr 26	28Apr-26	12 Apr 26 A	28Apr-26A	$000	$000	$0.0	0.0
MLTX02-004EN-992	Material Approval for Artificial TURF	3.0	100%	100%	28 Apr 26	30Apr-26	28 Apr 26 A	30Apr-26A	$000	$000	$0.0	0.0
RUBBER GRANULES		1400	0%	0%	06 May-26	21May-26	06 May 26 A	21May-26A	$000	$000	$0.0	0.0
MLTX02-004EN-977	Material Submittal for Rubber Granules	1.0	100%	100%	06 May-26	06May-26	06 May 26 A	06May-26A	$000	$000	$0.0	0.0
MLTX02-004EN-993	Material Approval for RubberGranules	1.0	100%	100%	21 May-26	21May-26	21 May 26 A	21May-26A	$000	$000	$0.0	0.0
PADELGLASS		1400	0%	0%	06 May-26	21May-26	06 May 26 A	21May-26A	$000	$000	$0.0	0.0

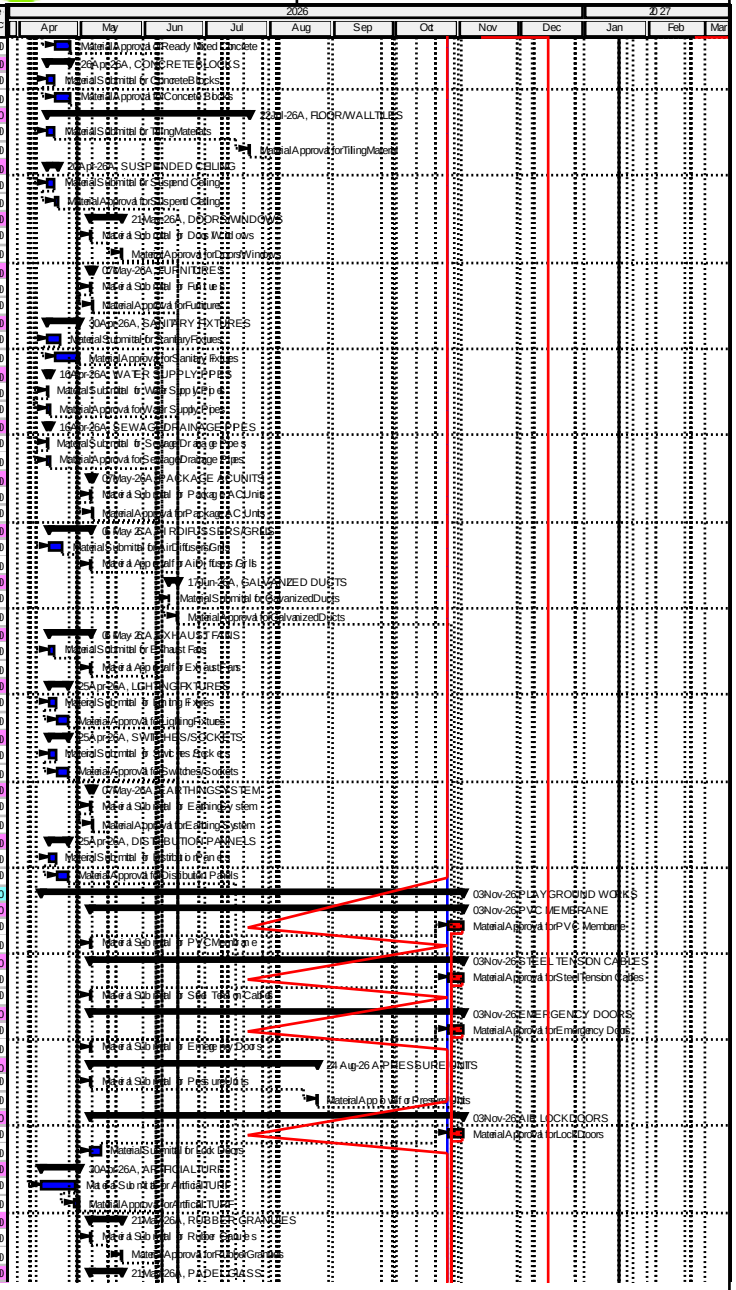

© Oracle Corporation

ActivityID	ActivityName	Orginal Duration	Schedule %	Performance% Complete	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Variance - BL Project
MLTX02-004EN-978	Material Submittal for Padel Glass	1.00	100%	100%	06-May-26	06-May-26	06 May 26 A	06-May-26A	$000	$000	$0.00	0.00
MLTX02-004EN-994	Material Approval for Padel Glass	1.00	100%	100%	21-May-26	21-May-26	21 May 26 A	21-May-26A	$000	$000	$0.00	0.00
PADEL WIRE MESH/STEEL SETS		136.00	0%	0%	25-May-26	12-Jul-26	25 May 26 A	03Nov-26	$000	$000	$0.00	-97.00
MLTX02-004EN-995	Material Approval for Wire Mesh/Steel Sets	7.00	100%	0%	05-Jul-26	12-Jul-26	27-Oct-26	03Nov-26	$000	$000	$0.00	0.00
MLTX02-004EN-975	Material Submittal for Wire Mesh/Steel Sets	1.00	100%	100%	25-May-26	25-May-26	25 May 26 A	25-May-26A	$000	$000	$0.00	0.00
PACKAGE ACUNITS		1.00	0%	0%	21-May-26	21-May-26	21 May 26 A	21-May-26A	$000	$000	$0.00	0.00
MLTX02-004EN-948	Material Submittal for Package ACUnits	1.00	100%	100%	21-May-26	21-May-26	21 May 26 A	21-May-26A	$000	$000	$0.00	0.00
MLTX02-004EN-949	Material Approval for Package AC Units	1.00	100%	100%	21-May-26	21-May-26	21 May 26 A	21-May-26A	$000	$000	$0.00	0.00
AIRDFUSSERS/GRILLS		21.00	0%	0%	13 Apr 26	06-May-26	13 Apr 26 A	06-May-26A	$000	$000	$0.00	0.00
MLTX02-004EN-950	Material Submittal for AirDiffusers/Grills	9.00	100%	100%	13 Apr 26	22-Apr-26	13 Apr 26 A	22-Apr-26A	$000	$000	$0.00	0.00
MLTX02-004EN-951	Material Approval for AirDifussers/Grills	1.00	100%	100%	06-May-26	06-May-26	06 May 26 A	06-May-26A	$000	$000	$0.00	0.00
AGGREGATE BASECOURSE		33.00	0%	0%	21-May-26	01Jul-26	21 May 26 A	01Jul-26A	$000	$000	$0.00	0.00
MLTX02-004EN-902	Material Submittal for AggegateBase Course	1.00	100%	100%	21-May-26	21-May-26	21 May 26 A	21-May-26A	$000	$000	$0.00	0.00
MLTX02-004EN-903	Material Approval for Aggregate Base Couse	1.00	100%	100%	01-Jul-26	01Jul-26	01 Jul-26A	01Jul-26A	$000	$000	$0.00	0.00
BITUMINOUS BASE &WEARING COURSE		2.00	0%	0%	16 Apr 26	18Apr-26	16 Apr 26 A	18Apr-26A	$000	$000	$0.00	0.00
MLTX02-004EN-904	Material Submittal for BituminousBase& Wearing Couce	2.00	100%	100%	16 Apr 26	18Apr-26	16 Apr 26 A	18Apr-26A	$000	$000	$0.00	0.00
MLTX02-004EN-905	Material Approval for the Site	1.00	100%	100%	18 Apr 26	18Apr-26	18 Apr 26 A	18Apr-26A	$000	$000	$0.00	0.00
INTERLOCKNG PAVING		1.00	0%	0%	21-May-26	21-May-26	21 May 26 A	21-May-26A	$000	$000	$0.00	0.00
MLTX02-004EN-906	Material Submittal for InterlockingBlockPavers	1.00	100%	100%	21-May-26	21-May-26	21 May 26 A	21-May-26A	$000	$000	$0.00	0.00
MLTX02-004EN-911	Material Approval for Interlocking Bbck Pavers	1.00	100%	100%	21-May-26	21-May-26	21 May 26 A	21-May-26A	$000	$000	$0.00	0.00
MARKINGPAINT		6.00	0%	0%	13 Apr 26	19Apr-26	13 Apr 26 A	19Apr-26A	$000	$000	$0.00	0.00
MLTX02-004EN-933	Material Submittal for Making Paint	5.00	100%	100%	13 Apr 26	18Apr-26	13 Apr 26 A	18Apr-26A	$000	$000	$0.00	0.00
MLTX02-004EN-996	Material Approval for Marking Paint	2.00	100%	100%	18 Apr 26	19Apr-26	18 Apr 26 A	19Apr-26A	$000	$000	$0.00	0.00
GALVANIZEDDUCTS		113.00	0%	0%	13 Jun 26	11Jul-26	13 Jun 26 A	08Aug-26A	$000	$000	$0.00	-24.00
MLTX02-004EN-952	Material Submittal for GalvanizedDuct	1.00	100%	100%	13 Jun 26	13Jun-26	13 Jun 26 A	13Jun-26A	$000	$000	$0.00	0.00
MLTX02-004EN-953	Material Approval for GalvanizedDuct	6.00	100%	100%	05-Jul-26	11Jul-26	08 Aug 26 A	08Aug-26A	$000	$000	$0.00	5.00
EXHAUSTFANS		21.00	0%	0%	13 Apr 26	06-May-26	13 Apr 26 A	06-May-26A	$000	$000	$0.00	0.00
MLTX02-004EN-954	Material Submittal for Exhaust Fans	5.00	100%	100%	13 Apr 26	18Apr-26	13 Apr 26 A	18Apr-26A	$000	$000	$0.00	0.00
MLTX02-004EN-955	Material Approval for Exhaust Fans	1.00	100%	100%	06-May-26	06-May-26	06 May 26 A	06-May-26A	$000	$000	$0.00	0.00
DISTRBUTON BOARDS		9.00	0%	0%	13 Apr 26	22Apr-26	13 Apr 26 A	22Apr-26A	$000	$000	$0.00	0.00
MLTX02-004EN-962	Material Submittal for DistributionBoards	3.00	100%	100%	13 Apr 26	15Apr-26	13 Apr 26 A	15Apr-26A	$000	$000	$0.00	0.00
MLTX02-004EN-963	Material Approval for Distibuton Boards	6.00	100%	100%	16 Apr 26	22Apr-26	16 Apr 26 A	22Apr-26A	$000	$000	$0.00	0.00
POWERCABLES		9.00	0%	0%	13 Apr 26	22Apr-26	13 Apr 26 A	22Apr-26A	$000	$000	$0.00	0.00
MLTX02-004EN-964	Material Submittal for PowerCables	3.00	100%	100%	13 Apr 26	15Apr-26	13 Apr 26 A	15Apr-26A	$000	$000	$0.00	0.00
MLTX02-004EN-965	Material Approval for PowerCables	6.00	100%	100%	16 Apr 26	22Apr-26	16 Apr 26 A	22Apr-26A	$000	$000	$0.00	0.00
LIGHTFKTURES		9.00	0%	0%	13 Apr 26	22Apr-26	13 Apr 26 A	22Apr-26A	$000	$000	$0.00	0.00
MLTX02-004EN-966	Material Submittal for Light Fixtures	3.00	100%	100%	13 Apr 26	15Apr-26	13 Apr 26 A	15Apr-26A	$000	$000	$0.00	0.00
MLTX02-004EN-967	Material Approval for Light Fixtures	6.00	100%	100%	16 Apr 26	22Apr-26	16 Apr 26 A	22Apr-26A	$000	$000	$0.00	0.00
CCTV MATERALS		9.00	0%	0%	13 Apr 26	22Apr-26	13 Apr 26 A	22Apr-26A	$000	$000	$0.00	0.00
MLTX02-004EN-968	Material Submittal for CCTV	3.00	100%	100%	13 Apr 26	15Apr-26	13 Apr 26 A	15Apr-26A	$000	$000	$0.00	0.00
MLTX02-004EN-969	Material Approval for CCTV	6.00	100%	100%	16 Apr 26	22Apr-26	16 Apr 26 A	22Apr-26A	$000	$000	$0.00	0.00
POWEROUTIETS/SWITCHES		2.00	0%	0%	06-May-26	07May-26	06 May 26 A	07May-26A	$000	$000	$0.00	0.00
MLTX02-004EN-970	Material Submittal for PowerOutlets/Switches	1.00	100%	100%	06-May-26	06May-26	06 May 26 A	06May-26A	$000	$000	$0.00	0.00
MLTX02-004EN-971	Material Approval for PowerOutlets/Switches	1.00	100%	100%	07-May-26	07May-26	07 May 26 A	07May-26A	$000	$000	$0.00	0.00
LANDSCAPE WORKS		98.00	0%	0%	07 Apr 26	18Jul-26	07 Apr 26 A	27Jul-26A	$000	$000	$0.00	-8.00
INTERLOCKNG PAVING		1.00	0%	0%	21-May-26	21May-26	21 May 26 A	21May-26A	$000	$000	$0.00	0.00
MLTX02-004EN-974	Material Submittal for InterlockingBlockPavers	1.00	100%	100%	21-May-26	21May-26	21 May 26 A	21May-26A	$000	$000	$0.00	0.00
MLTX02-004EN-975	Material Approval for Interlocking Bbck Pavers	1.00	100%	100%	21-May-26	21May-26	21 May 26 A	21May-26A	$000	$000	$0.00	0.00
CURBSTONE		1.00	0%	0%	21-May-26	21May-26	21 May 26 A	21May-26A	$000	$000	$0.00	0.00
MLTX02-004EN-984	Material Submittal for Cubstone	1.00	100%	100%	21-May-26	21May-26	21 May 26 A	21May-26A	$000	$000	$0.00	0.00
MLTX02-004EN-985	Material Approval for Curbstone	1.00	100%	100%	21-May-26	21May-26	21 May 26 A	21May-26A	$000	$000	$0.00	0.00
PAVEMENTMARKNG		6.00	0%	0%	13 Apr 26	19Apr-26	13 Apr 26 A	19Apr-26A	$000	$000	$0.00	0.00
MLTX02-004EN-907	Material Submittal for Pavement Makings	5.00	100%	100%	13 Apr 26	18Apr-26	13 Apr 26 A	18Apr-26A	$000	$000	$0.00	0.00
MLTX02-004EN-912	Material Approval for Pavement Makings	2.00	100%	100%	18 Apr 26	19Apr-26	18 Apr 26 A	19Apr-26A	$000	$000	$0.00	0.00
TRAFFC SIGNS		65.00	0%	0%	06-May-26	11Jul-26	06 May 26 A	18Jul-26A	$000	$000	$0.00	-6.00
MLTX02-004EN-908	Material Submittal for TrafficSigns	1.00	100%	100%	06-May-26	06May-26	06 May 26 A	06May-26A	$000	$000	$0.00	0.00
MLTX02-004EN-909	Material Approval for TrafficSigns	6.00	100%	100%	05-Jul-26	11Jul-26	13 Jul-26A	18Jul-26A	$000	$000	$0.00	5.00
IRRGATIONPIPESSPRINKIERS		93.00	0%	0%	13 Apr 26	18Jul-26	13 Apr 26 A	27Jul-26A	$000	$000	$0.00	-8.00
MLTX02-004EN-913	Material Submittal for Irrigation Pipes/Sprinkles	5.00	100%	100%	13 Apr 26	18Apr-26	13 Apr 26 A	18Apr-26A	$000	$000	$0.00	0.00
MLTX02-004EN-914	Material Approval for Irrigation Pipes/Sprinkles	6.00	100%	100%	12-Jul-26	18Jul-26	27 Jul-26A	27Jul-26A	$000	$000	$0.00	5.00
AGRICULTURE SOIL		14.00	0%	0%	06-May-26	06-May-26	06 May 26 A	21May-26A	$000	$000	$0.00	0.00
MLTX02-004EN-980	Material Submittal for Agriculture Soil	1.00	100%	100%	06-May-26	06May-26	06 May 26 A	06May-26A	$000	$000	$0.00	0.00
MLTX02-004EN-981	Material Approval for Agriculture Soil	1.00	100%	100%	21-May-26	21May-26	21 May 26 A	21May-26A	$000	$000	$0.00	0.00
TRACK SURFACE		14.00	0%	0%	06-May-26	21May-26	06 May 26 A	21May-26A	$000	$000	$0.00	0.00
MLTX02-004EN-982	Material Submittal for Track Suface	1.00	100%	100%	06-May-26	06May-26	06 May 26 A	06May-26A	$000	$000	$0.00	0.00
MLTX02-004EN-983	Material Approval for Track Surface	1.00	100%	100%	21-May-26	21May-26	21 May 26 A	21May-26A	$000	$000	$0.00	0.00
GRASS/TREES		14.00	0%	0%	06-May-26	21May-26	06 May 26 A	21May-26A	$000	$000	$0.00	0.00
MLTX02-004EN-986	Material Submittal for Grass/Trees	1.00	100%	100%	06-May-26	06May-26	06 May 26 A	06May-26A	$000	$000	$0.00	0.00
MLTX02-004EN-987	Material Approval for Grass/Trees	1.00	100%	100%	21-May-26	21May-26	21 May 26 A	21May-26A	$000	$000	$0.00	0.00
CABIES		9.00	0%	0%	13 Apr 26	22Apr-26	13 Apr 26 A	22Apr-26A	$000	$000	$0.00	0.00
MLTX02-004EN-972	Material Submittal for Cables	3.00	100%	100%	13 Apr 26	15Apr-26	13 Apr 26 A	15Apr-26A	$000	$000	$0.00	0.00
MLTX02-004EN-973	Material Approval for Cables	6.00	100%	100%	16 Apr 26	22Apr-26	16 Apr 26 A	22Apr-26A	$000	$000	$0.00	0.00

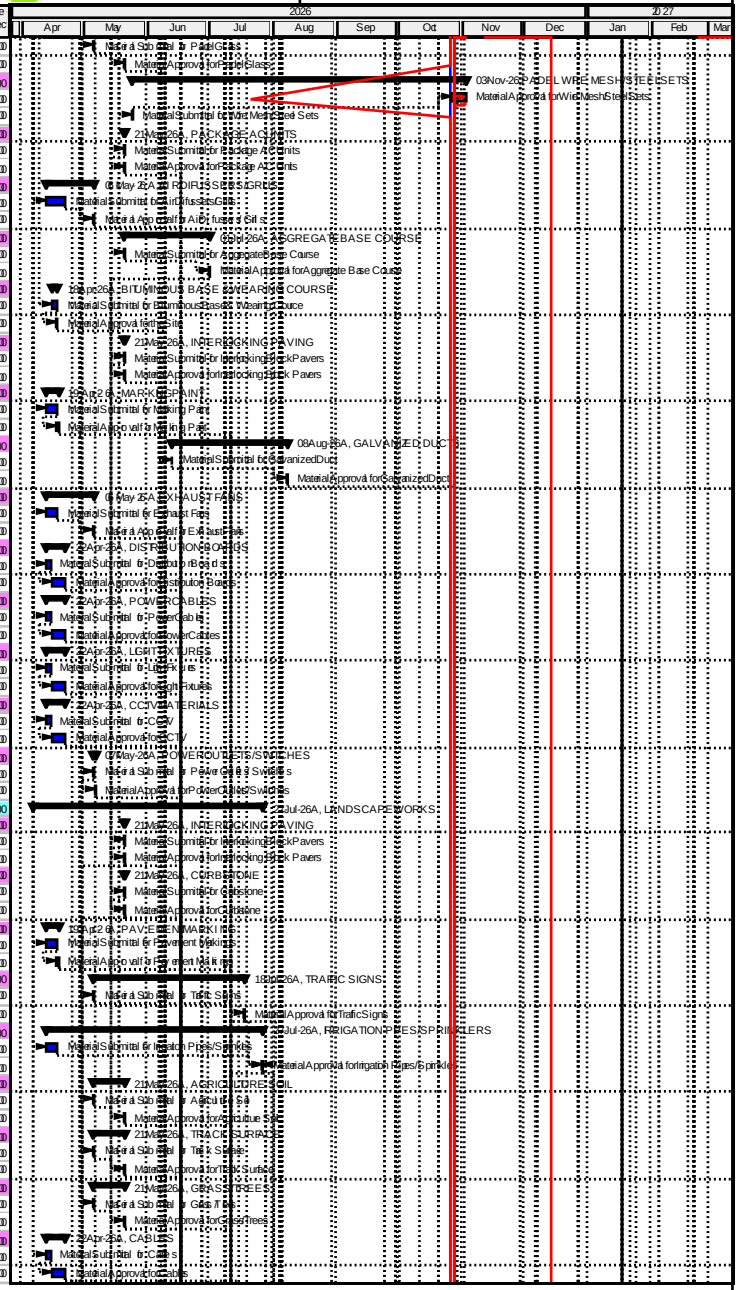


© Oracle Corporation

MLTX-02-004 - Playground Initiative for Western Region (Asir-Jazan -Jeddah)

Updateded schedule D.D 26-10-2026

ActivityID	ActivityName	Orginal Duration	Schedule %	Performance% Complete	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Variance - BL Project
	LIGHTPOLES	8.00	0%	0%	07-Apr-26	15-Apr-26	07-Apr-26 A	15-Apr-26A	$000	$000	$0.00	0.00
	MLTX-02-004EN-897	Material Submittal for Lightingpoles	3.00	100%	100%	13-Apr-26	15-Apr-26	13-Apr-26 A	15-Apr-26A	$000	$000	$0.00	0.00
	MLTX-02-004EN-898	Material Approval for Lightingpoles	1.00	100%	100%	07-Apr-26	07-Apr-26	07-Apr-26 A	07Apr-26A	$000	$000	$0.00	0.00
	PROCUREMENT		25200	0%	0%	06-May-26	07Nov-26	06 May-26 A	01Mar-27	$000	$000	$0.00	-9700
	SHORTLEAD ITEM		21300	0%	0%	06-May-26	21Oct-26	06 May-26 A	13Jan-27	$000	$000	$0.00	-7200
	TOILETSERVICE WORKS		18200	0%	0%	06-May-26	24Sep-26	06 May-26 A	18Nov-26	$000	$000	$0.00	-4700
	STEELREINFORCEMENT		1300	0%	0%	13-May-26	31May-26	13 May-26 A	31May-26A	$000	$000	$0.00	0.00
MLTX-02-00-4PR-9970	PO for Steel Reinforcement		2.00	100%	100%	13-May-26	14May-26	13 May-26 A	14May-26A	$000	$000	$0.00	0.00
MLTX-02-00-4PR-10070	Material Delivery of Steel Reinforcement		1.00	100%	100%	31-May-26	31May-26	31 May-26 A	31May-26A	$000	$000	$0.00	0.00
	CONCRETE BLOCKS		7200	0%	0%	06-May-26	09Jul-26	06 May-26 A	27Jul-26A	$000	$000	$0.00	-1500
MLTX-02-00-4PR-10150	PO for Concrete Blocks		1.00	100%	100%	06-May-26	06May-26	06 May-26 A	06May-26A	$000	$000	$0.00	0.00
MLTX-02-00-4PR-10160	Material Delivery of Concrete Blocks		5.00	100%	100%	05-Jul-26	09Jul-26	27-Jul-26A	27Jul-26A	$000	$000	$0.00	4.00
	FLOORWALL TILES		2800	0%	0%	19-Jul-26	08Aug-26	08 Aug-26 A	12Aug-26A	$000	$000	$0.00	13.00
MLTX-02-00-4PR-10170	PO for TillingMaterials		5.00	100%	100%	19-Jul-26	23Jul-26	08 Aug-26 A	08Aug-26A	$000	$000	$0.00	4.00
MLTX-02-00-4PR-10180	Material Delivery of TailingMaterial		1300	100%	100%	25-Jul-26	08Aug-26	12-Aug-26 A	12Aug-26A	$000	$000	$0.00	12.00
	SUSPENDED CELING		1800	0%	0%	05-Jul-26	25Jul-26	08 Aug-26 A	10Oct-26A	$000	$000	$0.00	-3600
MLTX-02-00-4PR-10190	PO for Suspend Celing		5.00	100%	100%	05-Jul-26	09Jul-26	08 Aug-26 A	08Aug-26A	$000	$000	$0.00	4.00
MLTX-02-00-4PR-10200	Material Delivery of SuspendCeiling		1300	100%	100%	11-Jul-26	25Jul-26	10-Oct-26 A	10Oct-26A	$000	$000	$0.00	12.00
	DOORS/WINDOWS		10700	0%	0%	24-Jun-26	15Jul-26	24-Jun-26 A	10Oct-26A	$000	$000	$0.00	-7300
MLTX-02-00-4PR-10210	PO for Doos/Windows		1.00	100%	100%	24-Jun-26	24Jun-26	24-Jun-26 A	24Jun-26A	$000	$000	$0.00	0.00
MLTX-02-00-4PR-10220	Material Delivery for Doos/Windows		1000	100%	100%	05-Jul-26	15Jul-26	10-Oct-26 A	10Oct-26A	$000	$000	$0.00	9.00
	WATERSUPPLYPIPES		1.00	0%	0%	13-Jun-26	13Jun-26	13-Jun-26 A	13Jun-26A	$000	$000	$0.00	0.00
MLTX-02-00-4PR-10250	PO for Water Supply Pipes		1.00	100%	100%	13-Jun-26	13Jun-26	13-Jun-26 A	13Jun-26A	$000	$000	$0.00	0.00
MLTX-02-00-4PR-10260	Material Delivery for Water Supply Pipes		1.00	100%	100%	13-Jun-26	13Jun-26	13-Jun-26 A	13Jun-26A	$000	$000	$0.00	0.00
	SEWAGEDRAINAGEPIPES		1.00	0%	0%	13-Jun-26	13Jun-26	13-Jun-26 A	13Jun-26A	$000	$000	$0.00	0.00
MLTX-02-00-4PR-10270	PO for Sewage/Drainage Pipes		1.00	100%	100%	13-Jun-26	13Jun-26	13-Jun-26 A	13Jun-26A	$000	$000	$0.00	0.00
MLTX-02-00-4PR-10280	Material Delivery for SewageDrainage Pipes		1.00	100%	100%	13-Jun-26	13Jun-26	13-Jun-26 A	13Jun-26A	$000	$000	$0.00	0.00
	SANITARYFIXTURES		12600	0%	0%	16-Jun-26	29Jul-26	16-Jun-26 A	03Aug-26A	$000	$000	$0.00	-400
MLTX-02-00-4PR-10230	PO for SanitaryFixtures		1.00	100%	100%	16-Jun-26	16Jun-26	16-Jun-26 A	16Jun-26A	$000	$000	$0.00	0.00
MLTX-02-00-4PR-10240	Material Delivery for SanitaryFixtues		1200	100%	100%	16-Jul-26	29Jul-26	03 Aug-26 A	03Aug-26A	$000	$000	$0.00	11.00
	PACKAGE ACUNITS		12300	0%	0%	16-Jun-26	10Aug-26	16-Jun-26 A	07Nov-26	$000	$000	$0.00	-7500
MLTX-02-00-4PR-10380	Material Delivery for Package AC Units		1000	100%	0%	30-Jul-26	10Aug-26	27-Oct-26	07Nov-26	$000	$000	$0.00	0.00
MLTX-02-00-4PR-10370	PO for Package AC Units		1.00	100%	100%	16-Jun-26	16Jun-26	16-Jun-26 A	16Jun-26A	$000	$000	$0.00	0.00
	AIRDIFUSSERS/ GRILLS		14600	0%	0%	16-Jun-26	22Aug-26	16-Jun-26 A	08Aug-26A	$000	$000	$0.00	12.00
MLTX-02-00-4PR-10390	PO for AirDiffusersGrills		1.00	100%	100%	16-Jun-26	16Jun-26	16-Jun-26 A	16Jun-26A	$000	$000	$0.00	0.00
MLTX-02-00-4PR-10400	Material Delivery for AirDiffusersGrills		1000	100%	100%	11-Aug-26	22Aug-26	08 Aug-26 A	08Aug-26A	$000	$000	$0.00	9.00
	GALVANIZED DUCTS		11700	0%	0%	16-Jun-26	19Jul-26	16-Jun-26 A	08Aug-26A	$000	$000	$0.00	-1700
MLTX-02-00-4PR-10410	PO for GalvanizedDucts		1.00	100%	100%	16-Jun-26	16Jun-26	16-Jun-26 A	16Jun-26A	$000	$000	$0.00	0.00
MLTX-02-00-4PR-10420	Material Delivery for GalvanizedDucts		1300	100%	100%	05-Jul-26	19Jul-26	08 Aug-26 A	08Aug-26A	$000	$000	$0.00	12.00
	EXHAUSTFANS		13200	0%	0%	16-Jun-26	05Aug-26	16-Jun-26 A	17Aug-26A	$000	$000	$0.00	-1000
MLTX-02-00-4PR-10430	PO for Exhaust Fans		1.00	100%	100%	16-Jun-26	16Jun-26	16-Jun-26 A	16Jun-26A	$000	$000	$0.00	0.00
MLTX-02-00-4PR-10440	Material Delivery for Exhaust Fans		1500	100%	100%	20-Jul-26	05Aug-26	17-Aug-26 A	17Aug-26A	$000	$000	$0.00	14.00
	LIGHTING FIXTURES		12800	0%	0%	16-Jun-26	23Aug-26	16-Jun-26 A	12Nov-26	$000	$000	$0.00	-6900
MLTX-02-00-4PR-10300	Material Delivery for LightingFixtures		1500	100%	0%	06-Aug-26	23Aug-26	27-Oct-26	12Nov-26	$000	$000	$0.00	0.00
MLTX-02-00-4PR-10290	PO for LightingFixtures		1.00	100%	100%	16-Jun-26	16Jun-26	16-Jun-26 A	16Jun-26A	$000	$000	$0.00	0.00
	SWITCHES/SOCKETS		14300	0%	0%	24-Jun-26	31Aug-26	24-Jun-26 A	10Oct-26A	$000	$000	$0.00	-3300
MLTX-02-00-4PR-10310	PO for Switches/Sockets		1.00	100%	100%	24-Jun-26	24Jun-26	24-Jun-26 A	24Jun-26A	$000	$000	$0.00	0.00
MLTX-02-00-4PR-10320	Material Delivery for Switches/Sockets		7.00	100%	100%	24-Aug-26	31Aug-26	05-Oct-26 A	10Oct-26A	$000	$000	$0.00	2.00
	EARTHINGSYSTEM		1.00	0%	0%	21-May-26	21May-26	21 May-26 A	21May-26A	$000	$000	$0.00	0.00
MLTX-02-00-4PR-10110	PO for EarthingSystem		1.00	100%	100%	21-May-26	21May-26	21 May-26 A	21May-26A	$000	$000	$0.00	0.00
MLTX-02-00-4PR-10120	Material Delivery for EarthingSystem		1.00	100%	100%	21-May-26	21May-26	21 May-26 A	21May-26A	$000	$000	$0.00	0.00
	DISTRBUTION PANNELS		9700	0%	0%	05-Jul-26	27Jul-26	22-Jul-26A	12Nov-26	$000	$000	$0.00	-7700
MLTX-02-00-4PR-10140	Material Delivery for Distibuton Panels		1500	100%	0%	11-Jul-26	27Jul-26	27-Oct-26	12Nov-26	$000	$000	$0.00	0.00
MLTX-02-00-4PR-10130	PO for DistributionPanels		5.00	100%	100%	05-Jul-26	09Jul-26	22-Jul-26A	22Jul-26A	$000	$000	$0.00	4.00
	FURNITURES		13300	0%	0%	16-Jun-26	24Sep-26	16-Jun-26 A	18Nov-26	$000	$000	$0.00	-4700
MLTX-02-00-4PR-10340	Material Delivery for Furnitues		2000	100%	0%	01-Sep-26	24Sep-26	27-Oct-26	18Nov-26	$000	$000	$0.00	0.00
MLTX-02-00-4PR-10330	PO for Furnitues		1.00	100%	100%	16-Jun-26	16Jun-26	16-Jun-26 A	16Jun-26A	$000	$000	$0.00	0.00
	PLAYGROUND WORKS		21200	0%	0%	07-May-26	21Oct-26	07 May-26 A	13Jan-27	$000	$000	$0.00	-7200
	PVC MEMBRANE		11700	0%	0%	16-Jun-26	08Jul-26	16-Jun-26 A	31Oct-26	$000	$000	$0.00	-9700
MLTX-02-00-4PR-10540	Material Delivery for PVC Membrane		4.00	100%	0%	05-Jul-26	08Jul-26	27-Oct-26	31Oct-26	$000	$000	$0.00	0.00
MLTX-02-00-4PR-10530	PO for PVC Membrane		1.00	100%	100%	16-Jun-26	16Jun-26	16-Jun-26 A	16Jun-26A	$000	$000	$0.00	0.00
	ARTIFICIAL TURF		12900	0%	0%	16-Jun-26	22Jul-26	16-Jun-26 A	14Nov-26	$000	$000	$0.00	-9700
MLTX-02-00-4PR-10780	Material Delivery for Artifical TURF		1200	100%	0%	09-Jul-26	22Jul-26	01-Nov-26	14Nov-26	$000	$000	$0.00	0.00
MLTX-02-00-4PR-10770	PO for Artifical TURF		1.00	100%	100%	16-Jun-26	16Jun-26	16-Jun-26 A	16Jun-26A	$000	$000	$0.00	0.00
	RUBBER GRANULES		14100	0%	0%	16-Jun-26	05Aug-26	16-Jun-26 A	28Nov-26	$000	$000	$0.00	-9700
MLTX-02-00-4PR-10800	Material Delivery for Rubber Granules		1200	100%	0%	23-Jul-26	05Aug-26	15-Nov-26	28Nov-26	$000	$000	$0.00	0.00
MLTX-02-00-4PR-10790	PO for Rubber Granules		1.00	100%	100%	16-Jun-26	16Jun-26	16-Jun-26 A	16Jun-26A	$000	$000	$0.00	0.00
	PADEL GLASS		15900	0%	0%	16-Jun-26	26Aug-26	16-Jun-26 A	19Dec-26	$000	$000	$0.00	-9700
MLTX-02-00-4PR-10820	Material Delivery for PadelGlass		1800	100%	0%	06-Aug-26	26Aug-26	29-Nov-26	19Dec-26	$000	$000	$0.00	0.00
MLTX-02-00-4PR-10810	PO for Padel Glass		1.00	100%	100%	16-Jun-26	16Jun-26	16-Jun-26 A	16Jun-26A	$000	$000	$0.00	0.00
	PADEL WIRE MESHSTEELSETS		17400	0%	0%	16-Jun-26	13Sep-26	16-Jun-26 A	05Jan-27	$000	$000	$0.00	-9700
MLTX-02-00-4PR-10840	Material Delivery for Wire MeshSteelSets		1500	100%	0%	27-Aug-26	13Sep-26	20-Dec-26	05Jan-27	$000	$000	$0.00	0.00
MLTX-02-00-4PR-10830	PO for Wire MeshSteelSets		1.00	100%	100%	16-Jun-26	16Jun-26	16-Jun-26 A	16Jun-26A	$000	$000	$0.00	0.00

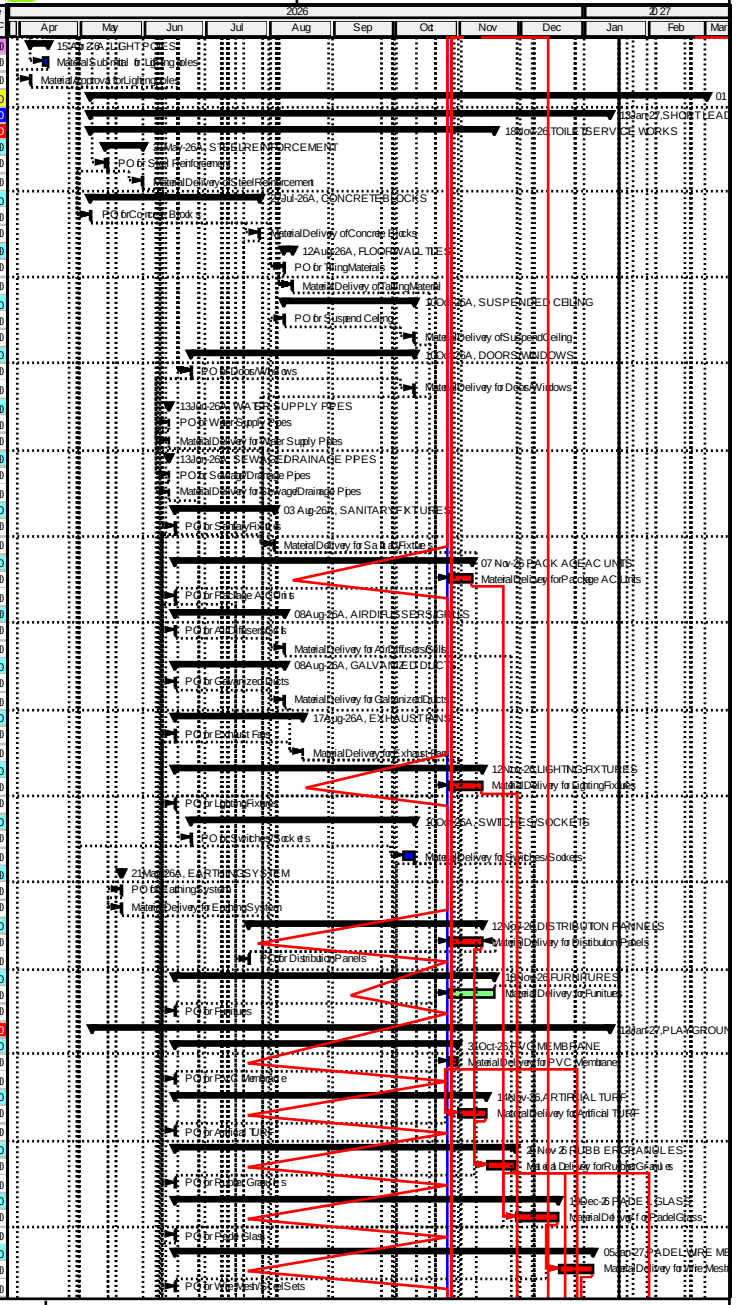


Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work

TASK filter: All Activities

© Oracle Corporation

ActivityID	ActivityName	Orginal Duration	Schedule %	Performance% Complete	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Variance - BL Project
	AGGREGATE BASECOURSE	1.0d	0%	0%	21-May-26	21-May-26	21-May-26 A	21-May-26A	$000	$000	$0.00	0.0d
MLTX02.0.4PR-9980	PO for AggregateBase Course	1.0d	100%	100%	21-May-26	21-May-26	21-May-26 A	21-May-26A	$000	$000	$0.00	0.0d
MLTX02.0.4PR-9990	MaterialDelivery for AggregateBase Course	1.0d	100%	100%	21-May-26	21-May-26	21-May-26 A	21-May-26A	$000	$000	$0.00	0.0d
	BITUMNOUS BASE &WEARING COURSE	7.0d	0%	0%	16-Jun-26	23-Jun-26	16-Jun-26A	23-Jun-26A	$000	$000	$0.00	0.0d
MLTX02.0.4PR-10000	PO for BituminousBase &Wearing Course	1.0d	100%	100%	16-Jun-26	16-Jun-26	16-Jun-26A	16-Jun-26A	$000	$000	$0.00	0.0d
MLTX02.0.4PR-10010	MaterialDelivery for theSite	1.0d	100%	100%	23-Jun-26	23-Jun-26	23-Jun-26A	23-Jun-26A	$000	$000	$0.00	0.0d
	INTERLOCKING PAVING	21200	0%	0%	07-May-26	21-Sep-26	07-May-26 A	13-Jan-27	$000	$000	$0.00	-9700
MLTX02.0.4PR-10030	MaterialDelivery for Interlocking Block Pavers	7.0d	100%	0%	14-Sep-26	21-Sep-26	06-Jan-27	13-Jan-27	$000	$000	$0.00	0.0d
MLTX02.0.4PR-10020	PO for InterlockingBlock Pavers	1.0d	100%	100%	07-May-26	07-May-26	07-May-26 A	07-May-26A	$000	$000	$0.00	0.0d
	MARKINGPAINT	9300	0%	0%	05-Jul-26	19-Jul-26	18-Jul-26A	03-Nov-26	$000	$000	$0.00	-8000
MLTX02.0.4PR-10360	MaterialDelivery for Marking Paint	7.0d	100%	0%	12-Jul-26	19-Jul-26	27-Oct-26	03-Nov-26	$000	$000	$0.00	0.0d
MLTX02.0.4PR-10350	PO for Making Paint	6.0d	100%	100%	05-Jul-26	11-Jul-26	18-Jul-26A	18-Jul-26A	$000	$000	$0.00	5.0d
	PACKAGE ACUNITS	13500	0%	0%	16-Jun-26	05-Aug-26	16-Jun-26A	21-Nov-26	$000	$000	$0.00	-9100
MLTX02.0.4PR-10460	MaterialDelivery for Package AC Units	1500	100%	0%	20-Jul-26	05-Aug-26	04-Nov-26	21-Nov-26	$000	$000	$0.00	0.0d
MLTX02.0.4PR-10450	PO for Package AC Units	1.0d	100%	100%	16-Jun-26	16-Jun-26	16-Jun-26A	16-Jun-26A	$000	$000	$0.00	0.0d
	AIRDIFUSSERS/ GRILLS	14100	0%	0%	16-Jun-26	23-Aug-26	16-Jun-26A	08-Aug-26A	$000	$000	$0.00	13.0d
MLTX02.0.4PR-10470	PO for AirDiffussersGrills	1.0d	100%	100%	16-Jun-26	16-Jun-26	16-Jun-26A	16-Jun-26A	$000	$000	$0.00	0.0d
MLTX02.0.4PR-10480	MaterialDelivery for AirDiffussers/Grills	1500	100%	100%	06-Aug-26	23-Aug-26	08-Aug-26 A	08-Aug-26A	$000	$000	$0.00	14.0d
	GALVANIZED D UCTS	15600	0%	0%	16-Jun-26	09-Sep-26	16-Jun-26A	08-Aug-26A	$000	$000	$0.00	28.0d
MLTX02.0.4PR-10490	PO for GalvanizedDuct	1.0d	100%	100%	16-Jun-26	16-Jun-26	16-Jun-26A	16-Jun-26A	$000	$000	$0.00	0.0d
MLTX02.0.4PR-10500	MaterialDelivery for GalvanizedDuct	1500	100%	100%	24-Aug-26	09-Sep-26	08-Aug-26 A	08-Aug-26A	$000	$000	$0.00	14.0d
	EXHAUST FANS	17100	0%	0%	16-Jun-26	28-Sep-26	16-Jun-26A	17-Aug-26A	$000	$000	$0.00	35.0d
MLTX02.0.4PR-10510	PO for Exhaust Fans	1.0d	100%	100%	16-Jun-26	16-Jun-26	16-Jun-26A	16-Jun-26A	$000	$000	$0.00	0.0d
MLTX02.0.4PR-10520	MaterialDelivery for Exhaust Fans	1500	100%	100%	10-Sep-26	28-Sep-26	17-Aug-26 A	17-Aug-26A	$000	$000	$0.00	14.0d
	DISTRBUTION BOARDS	9700	0%	0%	05-Jul-26	27-Jul-26	22-Jul-26A	12-Nov-26	$000	$000	$0.00	-7700
MLTX02.0.4PR-10640	MaterialDelivery for Distibuton Boards	1500	100%	0%	11-Jul-26	27-Jul-26	27-Oct-26	12-Nov-26	$000	$000	$0.00	0.0d
MLTX02.0.4PR-10630	PO for DistribuionBoards	5.0d	100%	100%	05-Jul-26	09-Jul-26	22-Jul-26A	22-Jul-26A	$000	$000	$0.00	4.0d
	POWERCABLES	7700	0%	0%	28-Jul-26	13-Aug-26	22-Jul-26A	07-Nov-26	$000	$000	$0.00	-7700
MLTX02.0.4PR-10660	MaterialDelivery for PowerCables	1000	100%	0%	03-Aug-26	13-Aug-26	27-Oct-26	07-Nov-26	$000	$000	$0.00	0.0d
MLTX02.0.4PR-10650	PO for PowerCables	5.0d	100%	100%	28-Jul-26	02-Aug-26	22-Jul-26A	22-Jul-26A	$000	$000	$0.00	4.0d
	LIGHTFIXTURES	2100	0%	0%	15-Aug-26	07-Sep-26	08-Nov-26	01-Dec-26	$000	$000	$0.00	0.0d
MLTX02.0.4PR-10670	PO for Light Fixtures	5.0d	100%	0%	15-Aug-26	19-Aug-26	08-Nov-26	12-Nov-26	$000	$000	$0.00	0.0d
MLTX02.0.4PR-10680	MaterialDelivery for Light Fixtures	1600	100%	0%	20-Aug-26	07-Sep-26	14-Nov-26	01-Dec-26	$000	$000	$0.00	0.0d
	CCTV MATERIA IS	3000	0%	0%	08-Sep-26	21-Oct-26	02-Dec-26	05-Jan-27	$000	$000	$0.00	7.0d
MLTX02.0.4PR-10690	PO for CCTV	1000	100%	0%	08-Sep-26	19-Sep-26	02-Dec-26	13-Dec-26	$000	$000	$0.00	0.0d
MLTX02.0.4PR-10700	MaterialDelivery for CCTV	2000	100%	0%	29-Sep-26	21-Oct-26	14-Dec-26	05-Jan-27	$000	$000	$0.00	0.0d
	POWEROUTLE TS/ SWITCHES	2100	0%	0%	20-Sep-26	14-Oct-26	14-Dec-26	06-Jan-27	$000	$000	$0.00	0.0d
MLTX02.0.4PR-10710	PO for PowerOutlets/Switches	6.0d	100%	0%	20-Sep-26	27-Sep-26	14-Dec-26	20-Dec-26	$000	$000	$0.00	0.0d
MLTX02.0.4PR-10720	MaterialDelivery for PowerOutlets/Switches	1500	100%	0%	28-Sep-26	14-Oct-26	21-Dec-26	06-Jan-27	$000	$000	$0.00	0.0d
	LANDSCAPE WORKS	17400	0%	0%	07-May-26	04-Oct-26	07-May-26 A	30-Nov-26	$000	$000	$0.00	-4900
	INTERLOCKING PAVING	15400	0%	0%	07-May-26	15-Jul-26	07-May-26 A	07-Nov-26	$000	$000	$0.00	-9700
MLTX02.0.4PR-10760	MaterialDelivery for Interlocking Block Pavers	1000	100%	0%	05-Jul-26	15-Jul-26	27-Oct-26	07-Nov-26	$000	$000	$0.00	0.0d
MLTX02.0.4PR-10750	PO for InterlockingBlock Pavers	1.0d	100%	100%	07-May-26	07-May-26	07-May-26 A	07-May-26A	$000	$000	$0.00	0.0d
	CURBSTONE	15400	0%	0%	07-May-26	15-Jul-26	07-May-26 A	07-Nov-26	$000	$000	$0.00	-9700
MLTX02.0.4PR-10900	MaterialDelivery for Curbstone	1000	100%	0%	05-Jul-26	15-Jul-26	27-Oct-26	07-Nov-26	$000	$000	$0.00	0.0d
MLTX02.0.4PR-10890	PO for Cubstone	1.0d	100%	100%	07-May-26	07-May-26	07-May-26 A	07-May-26A	$000	$000	$0.00	0.0d
	PAVEMENT MARKNG	8600	0%	0%	16-Jul-26	02-Aug-26	18-Jul-26A	07-Nov-26	$000	$000	$0.00	-8100
MLTX02.0.4PR-10050	MaterialDelivery for Pavement Makings	1000	100%	0%	22-Jul-26	02-Aug-26	27-Oct-26	07-Nov-26	$000	$000	$0.00	0.0d
MLTX02.0.4PR-10040	PO for Pavement Makings	5.0d	100%	100%	16-Jul-26	21-Jul-26	18-Jul-26A	18-Jul-26A	$000	$000	$0.00	4.0d
	TRAFFIC SIGNS	8500	0%	0%	03-Aug-26	18-Aug-26	18-Jul-26A	05-Nov-26	$000	$000	$0.00	-8100
MLTX02.0.4PR-10080	MaterialDelivery for TrafficSigns	9.0d	100%	0%	09-Aug-26	18-Aug-26	27-Oct-26	05-Nov-26	$000	$000	$0.00	0.0d
MLTX02.0.4PR-10060	PO for TrafficSigns	5.0d	100%	100%	03-Aug-26	08-Aug-26	18-Jul-26A	18-Jul-26A	$000	$000	$0.00	4.0d
	IRRGATION PIPESSPRINKLERS	9600	0%	0%	19-Aug-26	04-Oct-26	18-Jul-26A	19-Aug-26A	$000	$000	$0.00	10.0d
MLTX02.0.4PR-10090	PO for Irrigaton Pipes/Spimkles	5.0d	100%	100%	19-Aug-26	24-Aug-26	18-Jul-26A	18-Jul-26A	$000	$000	$0.00	4.0d
MLTX02.0.4PR-10100	MaterialDelivery for Irrigaton Pipes/Spimkles	8.0d	100%	100%	26-Sep-26	04-Oct-26	19-Aug-26 A	19-Aug-26A	$000	$000	$0.00	7.0d
	AGRICULTURE SOL	9800	0%	0%	05-Jul-26	23-Jul-26	18-Jul-26A	09-Nov-26	$000	$000	$0.00	-8100
MLTX02.0.4PR-10860	MaterialDelivery for Agriculture Sol	1200	100%	0%	11-Jul-26	23-Jul-26	27-Oct-26	09-Nov-26	$000	$000	$0.00	0.0d
MLTX02.0.4PR-10850	PO for Agriculture Sol	5.0d	100%	100%	05-Jul-26	09-Jul-26	18-Jul-26A	18-Jul-26A	$000	$000	$0.00	4.0d
	TRACK SURFACE	12800	0%	0%	24-Jun-26	04-Aug-26	24-Jun-26A	21-Nov-26	$000	$000	$0.00	-9200
MLTX02.0.4PR-10880	MaterialDelivery for Track Surface	1000	100%	0%	25-Jul-26	04-Aug-26	10-Nov-26	21-Nov-26	$000	$000	$0.00	0.0d
MLTX02.0.4PR-10870	PO for Track Suface	1.0d	100%	100%	24-Jun-26	24-Jun-26	24-Jun-26A	24-Jun-26A	$000	$000	$0.00	0.0d
	GRASS/TREES	7900	0%	0%	05-Aug-26	27-Aug-26	18-Jul-26A	12-Nov-26	$000	$000	$0.00	-8100
MLTX02.0.4PR-10920	MaterialDelivery for Grass/Trees	1500	100%	0%	11-Aug-26	27-Aug-26	27-Oct-26	12-Nov-26	$000	$000	$0.00	0.0d
MLTX02.0.4PR-10910	PO for Grass/Trees	5.0d	100%	100%	05-Aug-26	10-Aug-26	18-Jul-26A	18-Jul-26A	$000	$000	$0.00	4.0d
	CABLES	11200	0%	0%	22-Jul-26	14-Sep-26	22-Jul-26A	30-Nov-26	$000	$000	$0.00	-6500
MLTX02.0.4PR-10740	MaterialDelivery for Cables	1500	100%	0%	29-Aug-26	14-Sep-26	14-Nov-26	30-Nov-26	$000	$000	$0.00	0.0d
MLTX02.0.4PR-10730	PO for Cables	5.0d	100%	100%	22-Jul-26	27-Jul-26	22-Jul-26A	22-Jul-26A	$000	$000	$0.00	4.0d
LONG LEAD ITEM		22300	0%	0%	13-Jun-26	07-Nov-26	13-Jun-26A	01-Mar-27	$000	$000	$0.00	-9700
PLAYGROUND WORKS		19300	0%	0%	13-Jun-26	06-Oct-26	13-Jun-26A	24-Jan-27	$000	$000	$0.00	-9400
	STEELTENSION CABLES	17000	0%	0%	13-Jun-26	05-Sep-26	13-Jun-26A	28-Dec-26	$000	$000	$0.00	-9700
MLTX02.0.4PR-10560	MaterialDelivery for Steel Tension Cables	3000	100%	0%	25-Jul-26	27-Aug-26	16-Nov-26	20-Dec-26	$000	$000	$0.00	0.0d
MLTX02.0.4PR-10930	MaterialFabricationforSteelTension Cables	1000	100%	0%	13-Jul-26	23-Jul-26	04-Nov-26	15-Nov-26	$000	$000	$0.00	0.0d
MLTX02.0.4PR-10970	Staging time	7.0d	100%	0%	29-Aug-26	05-Sep-26	21-Dec-26	28-Dec-26	$000	$000	$0.00	0.0d

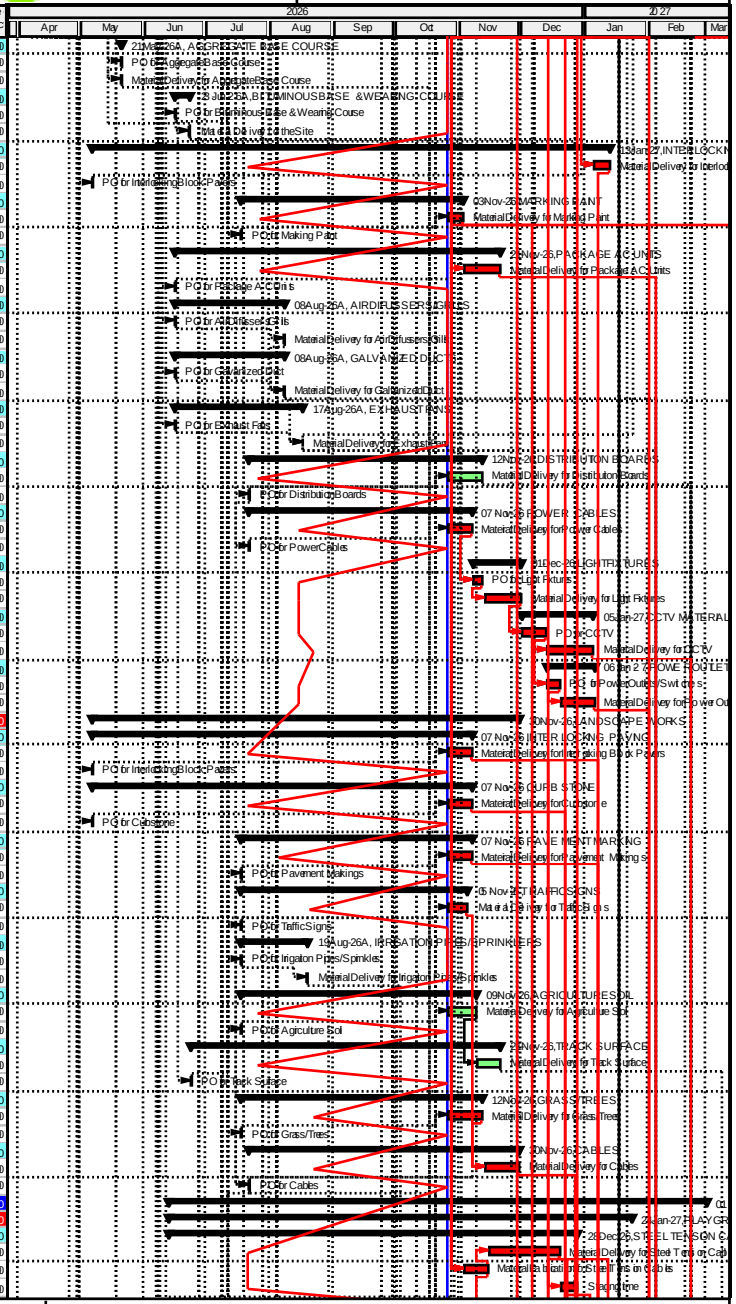


Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work

TASK filter: All Activities

© Oracle Corporation

ActivityID	ActivityName	Orginal Duration	Schedule %	Performance% Complete	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Variance - BL Project
MLTX02-004-PR-10550	PO for Steel Tension Cables	1.00	100%	100%	13-Jun-26	13-Jun-26A	13-Jun-26A	13-Jun-26A	$000	$000	$0.00	0.00
EMERGENCY DOORS		140.00	0%	0%	28-Jul-26	10-Sep-26	18-Jul-26A	03-Jan-27	$000	$000	$0.00	-106.00
MLTX02-004-PR-10580	Material Delivery for Emergency Doors	15.00	100%	0%	15-Aug-26	31-Aug-26	08-Nov-26	24-Nov-26	$000	$000	$0.00	0.00
MLTX02-004-PR-10940	Material Fabrication for Emergency Doors	10.00	100%	0%	03-Aug-26	13-Aug-26	27-Oct-26	07-Nov-26	$000	$000	$0.00	0.00
MLTX02-004-PR-10980	Staging time	5.00	100%	0%	06-Sep-26	10-Sep-26	29-Dec-26	03-Jan-27	$000	$000	$0.00	0.00
MLTX02-004-PR-10570	PO for Emergency Doors	5.00	100%	100%	28-Jul-26	02-Aug-26	18-Jul-26A	18-Jul-26A	$000	$000	$0.00	4.00
PRESSURE UNITS		60.00	0%	0%	28-Jul-26	06-Oct-26	27-Oct-26	04-Jan-27	$000	$000	$0.00	0.00
MLTX02-004-PR-10590	PO for Pressure Units	10.00	100%	0%	28-Jul-26	08-Aug-26	27-Oct-26	07-Nov-26	$000	$000	$0.00	0.00
MLTX02-004-PR-10600	Material Delivery for Pressure Units	25.00	100%	0%	01-Sep-26	30-Sep-26	01-Dec-26	29-Dec-26	$000	$000	$0.00	0.00
MLTX02-004-PR-10950	Material Fabrication for Pressure Units	20.00	100%	0%	09-Aug-26	31-Aug-26	08-Nov-26	30-Nov-26	$000	$000	$0.00	0.00
MLTX02-004-PR-10990	Staging time	5.00	100%	0%	01-Oct-26	06-Oct-26	30-Dec-26	04-Jan-27	$000	$000	$0.00	0.00
AIRLOCK DOORS		60.00	0%	0%	25-Jul-26	03-Oct-26	16-Nov-26	24-Jan-27	$000	$000	$0.00	0.00
MLTX02-004-PR-10610	PO for Lock Doors	10.00	100%	0%	25-Jul-26	04-Aug-26	16-Nov-26	26-Nov-26	$000	$000	$0.00	0.00
MLTX02-004-PR-10620	Material Delivery for Lock Doors	25.00	100%	0%	29-Aug-26	27-Sep-26	21-Dec-26	18-Jan-27	$000	$000	$0.00	0.00
MLTX02-004-PR-10960	Material Fabrication for Lock Doors	20.00	100%	0%	05-Aug-26	27-Aug-26	28-Nov-26	20-Dec-26	$000	$000	$0.00	0.00
MLTX02-004-PR-11000	Staging time	5.00	100%	0%	28-Sep-26	03-Oct-26	19-Jan-27	24-Jan-27	$000	$000	$0.00	0.00
LANDSCAPE WORKS		218.00	0%	0%	18-Jun-26	07-Nov-26	18-Jun-26A	01-Mar-27	$000	$000	$0.00	-97.00
LIGHTPOLES		218.00	0%	0%	18-Jun-26	07-Nov-26	18-Jun-26A	01-Mar-27	$000	$000	$0.00	-97.00
MLTX02-004-PR-9950	Material Fabrication for Lighting poles	30.00	100%	0%	29-Aug-26	03-Oct-26	21-Dec-26	24-Jan-27	$000	$000	$0.00	0.00
MLTX02-004-PR-9960	Material Delivery for Lighting poles	25.00	80%	0%	04-Oct-26	01-Nov-26	25-Jan-27	23-Feb-27	$000	$000	$0.00	0.00
MLTX02-004-PR-11010	Staging time	5.00	0%	0%	02-Nov-26	07-Nov-26	24-Feb-27	01-Mar-27	$000	$000	$0.00	0.00
MLTX02-004-PR-9940	PO for Lighting poles	1.00	100%	100%	18-Jun-26	18-Jun-26	18-Jun-26A	18-Jun-26A	$000	$000	$0.00	0.00
CONSTRUCTION PHASE		318.00	3923%	2889%	02-May-26	25-Jan-27	02-May-26A	19-May-27	$4190.27	$3085.78928	$10680.07	-91.00
SITEWORKS		318.00	3097%	2644%	02-May-26	25-Jan-27	02-May-26A	19-May-27	$2911.16	$2485.57574	$9399.93	-91.00
EARTH WORKS		109.00	100%	100%	02-May-26	23-Jul-26	02-May-26A	10-Oct-26A	$542.46	$542.46	$542.46	-66.00
MLTX02-004-CN-11180	Excavation(inall types of soil) including Compaction(PlaygoundArea)	8.25	100%	100%	02-May-26	11-May-26	02-May-26A	11-May-26A	$133.09	$133.09	$133.09	0.00
MLTX02-004-CN-11190	Excavation(inall types of soil) including Compaction(Service/ToiletBuilding)	12.03	100%	100%	07-May-26	21-May-26	07-May-26A	21-May-26A	$32.32	$32.32	$32.32	0.00
MLTX02-004-CN-11190	Excavation(inall types of soil) including Compaction(Landscape Area)	14.14	100%	100%	06-May-26	23-May-26	06-May-26A	23-May-26A	$202.99	$202.99	$202.99	0.00
MLTX02-004-CN-11910	Backfilling onLayers(Selected Soil)including Compaction (Playground Area)	32.00	100%	100%	25-May-26	04-Jul-26	25-May-26A	04-Jul-26A	$22.18	$22.18	$22.18	0.00
MLTX02-004-CN-11920	Backfilling onLayers(Selected Soil)including Compaction (Service/ToiletBuilding)	14.20	100%	100%	25-May-26	14-Jun-26	25-May-26A	14-Jun-26A	$8.19	$8.19	$8.19	0.00
MLTX02-004-CN-11930	Backfilling onLayers(Selected Soil)including Compaction (LandscapeArea)	9.00	100%	100%	05-Jul-26	14-Jul-26	29-Aug-26A	10-Oct-26A	$87.01	$87.01	$87.01	-27.00
MLTX02-004-CN-11910R	Backfilling onLayers(Selected Soil)including Compaction (Playground Area)Remain	8.00	100%	100%	15-Jul-26	23-Jul-26	05-Jul-26A	22-Aug-26A	$56.64	$56.68	$56.64	-33.00
LANDSCAPE WORKS		222.00	2704%	2218%	05-Jul-26	25-Jan-27	15-Jul-26A	19-May-27	$2368.71	$1943.12886	$8359.98	-82.00
PLAYGROUND AREA		164.00	6215%	157%	05-Jul-26	16-Jan-27	01-Oct-26A	06-May-27	$752.14	$190.125	$1210.72	-16.00
FOOTBALLPLAYGROUND		114.00	75%	20%	05-Jul-26	07-Dec-26	01-Oct-26A	06-Mar-27	$258.62	$69.03	$346.15	0.00
MLTX02-004-CN-1210	Finishingand SufaceFinish Works (Football Playground)	30.00	100%	0%	12-Sep-26	17-Oct-26	04-Jan-27	07-Feb-27	$143.81	$0.00	$148.81	2.50
MLTX02-004-CN-1210	Install Sport Equipments -Goal /Nets- Football Playground)	8.00	0%	0%	29-Nov-26	07-Dec-26	25-Feb-27	06-Mar-27	$0.00	$0.00	$7.19	0.00
MLTX02-004-CN-1210	Surface Makingand Painting(FootballPlaygound)	8.00	0%	0%	29-Nov-26	07-Dec-26	25-Feb-27	06-Mar-27	$0.00	$0.00	$14.38	1.25
MLTX02-004-CN-1210	Backfilling andCompacton ofBaseLayers(FootballPlaygound)	25.00	100%	20%	25-Jul-26	22-Aug-26	24-Oct-26A	24-Nov-26	$5.52	$1.15	$57.52	-3.00
MLTX02-004-CN-1210	Preparation andProofing for Subgade (Football Playground)	17.00	100%	100%	05-Jul-26	23-Jul-26	01-Oct-26A	19-Oct-26A	$5.52	$5.75	$57.52	1.00
PADELPLAYGROUND		126.00	6167%	39%	25-Jul-26	22-Dec-26	01-Oct-26A	12-Apr-27	$1.32	$0.36	$2.16	-33.00
MLTX02-004-CN-1210	Finishingand SufaceFinish Works (Padel Playground)	30.00	2667%	0%	18-Oct-26	21-Nov-26	08-Feb-27	18-Mar-27	$1.48	$0.00	$53.62	5.00
MLTX02-004-CN-1210	Install Sport Equipments -Goal /Nets- Padel Playground)	13.00	0%	0%	29-Nov-26	13-Dec-26	20-Mar-27	03-Apr-27	$0.00	$0.00	$32.17	5.00
MLTX02-004-CN-1210	Surface Makingand Painting(PadelPlaygound)	8.00	0%	0%	14-Dec-26	22-Dec-26	04-Apr-27	12-Apr-27	$0.00	$0.00	$10.72	5.00
MLTX02-004-CN-1210	Backfilling andCompacton ofBaseLayers(PadelPlaygound)	20.00	100%	20%	23-Aug-26	14-Sep-26	24-Oct-26A	24-Nov-26	$4.29	$0.86	$42.90	-8.00
MLTX02-004-CN-1210	Preparation andProofing for Subgade PadelPlayground)	25.00	100%	100%	25-Jul-26	22-Aug-26	01-Oct-26A	19-Oct-26A	$7.50	$7.50	$75.07	9.00
BASKETBALLPLAYGROUND		101.00	3369%	12%	23-Aug-26	22-Dec-26	01-Oct-26A	12-Apr-27	$1.05	$0.74	$3.12	-58.00
MLTX02-004-CN-1220	Finishingand SufaceFinish Works (Basketball Playground)	30.00	1667%	0%	21-Oct-26	24-Nov-26	29-Dec-26	01-Feb-27	$4.27	$0.00	$1.56	0.00
MLTX02-004-CN-1220	Install Sport Equipments -Goal /Nets- Basketball Playground)	10.00	0%	0%	08-Dec-26	19-Dec-26	07-Mar-27	21-Mar-27	$0.00	$0.00	$7.80	0.00
MLTX02-004-CN-1220	Surface Makingand Painting(BasketballPlaygound)	8.00	0%	0%	14-Dec-26	22-Dec-26	04-Apr-27	12-Apr-27	$0.00	$0.00	$15.60	0.00
MLTX02-004-CN-1210	Backfilling andCompacton ofBaseLayers(BasketballPlaygound)	30.00	100%	20%	15-Sep-26	20-Oct-26	24-Oct-26A	30-Nov-26	$3.12	$0.62	$31.20	-3.00
MLTX02-004-CN-1210	Preparation andProofing for Subgade PadelPlayground)	20.00	100%	100%	23-Aug-26	14-Sep-26	01-Oct-26A	19-Oct-26A	$3.12	$3.12	$31.20	4.00
PADELIENCE		21.00	0%	0%	23-Dec-26	16-Jan-27	13-Apr-27	06-May-27	$0.00	$0.00	$8.28	0.00
MLTX02-004-CN-1220	ExcavationforFence	3.00	0%	0%	23-Dec-26	26-Dec-26	13-Apr-27	15-Apr-27	$0.00	$0.00	$8.28	7.50
MLTX02-004-CN-1220	Concete Roundation for Fence including PostsFixaiton	4.00	0%	0%	27-Dec-26	30-Dec-26	17-Apr-27	20-Apr-27	$0.00	$0.00	$16.57	5.00
MLTX02-004-CN-1220	Tempered Glass Fenc Installaton and Fixation	5.00	0%	0%	05-Jan-27	10-Jan-27	25-Apr-27	01-May-27	$0.00	$0.00	$33.15	0.00
MLTX02-004-CN-1220	Chain LinkFenceInstallation andFixation	5.00	0%	0%	05-Jan-27	10-Jan-27	25-Apr-27	01-May-27	$0.00	$0.00	$16.57	5.00
MLTX02-004-CN-1220	Install of Fence Gates	5.00	0%	0%	11-Jan-27	16-Jan-27	02-May-27	06-May-27	$0.00	$0.00	$4.14	3.75
MLTX02-004-CN-1220	Backfilling andReinstatementforConcete Fundation	4.00	0%	0%	31-Dec-26	04-Jan-27	21-Apr-27	25-Apr-27	$0.00	$0.00	$4.14	3.75
CURBSTONE/INTERLOCK		83.00	100%	0%	27-Sep-26	24-Oct-26	27-Oct-26	31-Jan-27	$2.56	$1.97.50	$000	$2.56	1.97.50	-59.00
MLTX02-004-CN-1150	Interlock Installaton (Grey Scale)forLandScape(InludingFinishingWorks)	15.00	100%	0%	07-Oct-26	24-Oct-26	14-Jan-27	31-Jan-27	$1.85	$0.00	$1.85	0.00
MLTX02-004-CN-1220	Concete WorksUnder Curbstone	5.00	100%	0%	27-Sep-26	01-Oct-26	27-Oct-26	01-Nov-26	$1.59	$0.00	$15.90	0.00
MLTX02-004-CN-1220	CurbstoneInstalation	4.00	0%	0%	03-Oct-26	06-Oct-26	29-Dec-26	02-Jan-27	$5.40	$7.50	$000	$5.43	07.50	7.50
AIRDOME		180.00	22%	213%	15-Sep-26	26-Dec-26	15-Jul-26A	28-Mar-27	$1233.37	$1194.13125	$5696.25	-128.00
CIVIL WORKS		145.00	5238%	5071%	15-Sep-26	15-Nov-26	15-Jul-26A	10-Feb-27	$1233.37	$1194.13125	$2354.63	-128.00
MLTX02-004-CN-1220	Install of Membane CoveringSystem (AirDome)	4.00	0%	0%	08-Nov-26	11-Nov-26	08-Feb-27	07-Feb-27	$000	$000	$5.60	5.25
MLTX02-004-CN-1220	Themal Insulaton Works (Air Dome)	3.00	0%	0%	12-Nov-26	15-Nov-26	08-Feb-27	10-Feb-27	$000	$000	$5.60	5.25
MLTX02-004-CN-1220	Cable System Installaton (Air Dome)	3.00	100%	93%	27-Sep-26	29-Sep-26	24-Sep-26A	28-Dec-26	$5.60	$5.25	$521.38	$5.60	5.25	-7.90
MLTX02-004-CN-1220	ExcavationforFoundaiton & Playgound Aea (Air Dome)	5.00	100%	100%	15-Sep-26	20-Sep-26	15-Jul-26A	15-Aug-26A	$2.80	$2.80	$28.03	$2.80	12.50	-2.10
MLTX02-004-CN-1220	Concete Worksfor Roundations including Anchor Bolts (Air Dome)	4.00	100%	100%	21-Sep-26	26-Sep-26	29-Jul-26A	22-Sep-26A	$3.92	$3.92	$39.24	$3.92	37.50	-4.40
MECHANICALWORKS		13.00	0%	0%	16-Nov-26	30-Nov-26	11-Feb-27	27-Feb-27	$000	$000	$1.12	$1.25	0.00	0.00
MLTX02-004-CN-1220	AirDuctsand GrillsInstallation (Air Dome)	10.00	0%	0%	16-Nov-26	26-Nov-26	11-Feb-27	23-Feb-27	$000	$000	$2.80	3.12.50		

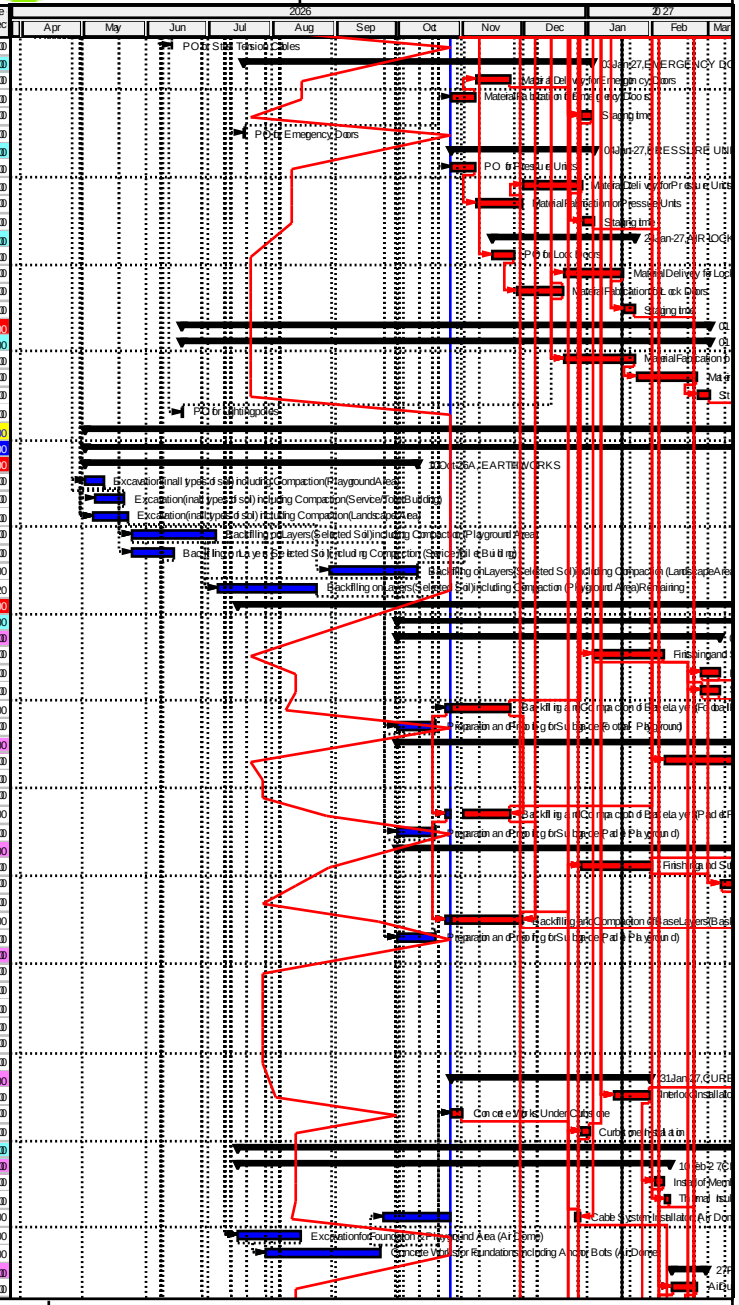

© Oracle Corporation

MLTX-02-004 - Playground Initiative for Western Region (Asir-Jazan -Jeddah)

Updateded schedule D.D 26-10-2026

ActivityID	ActivityName	Orginal Duration	Schedule %	Performance% Complete	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Variance - BL Project
MLTX02-004CN-122	AirUnitsInstallaton (Air Dome)	1300	0%	0%	16 Nov-26	30Nov-26	11 Feb 27	27Feb-27	$000	$000	$4 485 00.00	0.00
MLTX02-004CN-122	Exhaust Fans andDucts Instalation (Air Dome)	1100	0%	0%	16 Nov-26	28Nov-26	11 Feb 27	24Feb-27	$000	$000	$3 924 37.50	0.00
	EIECTRCAL WORKS	2200	0%	0%	01 Dec-26	26Dec-26	28 Feb 27	28Mar-27	$000	$000	$1 681 8 750 0	0.00
MLTX02-004CN-122	Light FktureWorks(AirDome)	2000	0%	0%	01 Dec-26	23Dec-26	28 Feb 27	25Mar-27	$000	$000	$2 803 12.50	0.00
MLTX02-004CN-122	Distibution Board and ElecticalWoks (Air Dome)	1800	0%	0%	01 Dec-26	21Dec-26	28 Feb 27	23Mar-27	$000	$000	$2 803 12.50	0.00
MLTX02-004CN-124	External ElecticalConnection Woks (Air Dome)	2000	0%	0%	01 Dec-26	23Dec-26	28 Feb 27	25Mar-27	$000	$000	$2 803 12.50	0.00
MLTX02-004CN-124	Emergency GeneratorInstallaton (AirDome)	2000	0%	0%	01 Dec-26	23Dec-26	28 Feb 27	25Mar-27	$000	$000	$5 606 25.00	0.00
MLTX02-004CN-124	Contol System Installation(AirDome)	2200	0%	0%	01 Dec-26	26Dec-26	28 Feb 27	28Mar-27	$000	$000	$2 803 12.50	0.00
	FINISHES WORKS	2500	0%	0%	19 Nov-26	17Dec-26	15 Feb 27	20Mar-27	$000	$000	$4 485 00.00	0.00
MLTX02-004CN-122	Doos Installation Including Emegency,Entrance doors (Air Dome)	1000	0%	0%	19 Nov-26	30Nov-26	15 Feb 27	27Feb-27	$000	$000	$2 242 50.00	0.00
MLTX02-004CN-122	Logoand Signs Installation(AirDome)	1500	0%	0%	01 Dec-26	17Dec-26	28 Feb 27	20Mar-27	$000	$000	$2 242 50.00	0.00
	IRRGATION NETWORK	4600	8276%	654%	07 Oct 26	01Nov-26	10 Oct26A	27Jan-27	$2 215 20 00	$175045 00	$2 676 70.00	-7300
MLTX02-004CN-13210	Installing ofValvesand fittings for IrigationNetwork	4.00	100%	0%	19 Oct 26	22Oct-26	14 Dec 26	17Dec-26	$4 617 5 00	$000	$46475.00	0.00
MLTX02-004CN-13220	Installing ofBubblers andSprayers	3.00	0%	0%	29 Oct 26	01Nov-26	25 Jan 27	27Jan-27	$000	$000	$46150.00	0.00
MLTX02-004CN-13190	Installing ofHDPE Pipes forIrrigation Network (Main Line)	5.00	100%	100%	07 Oct 26	12Oct-26	10 Oct26A	15Oct-26A	$8 079 5 00	$8 079 5.00	$80795.00	-100
MLTX02-004CN-13200	Installing ofHDPE Pipes forIrrigation Network (BranchLines)	5.00	100%	100%	13 Oct 26	18Oct-26	22 Oct26A	25Oct-26A	$9 425 0 00	$9 425 0.00	$94250.00	2.00
	NATURALGROUND	5.00	60%	0%	24 Oct 26	28Oct-26	19 Jan 27	24Jan-27	$4 617 4 75	$000	$80291.25	0.00
MLTX02-004CN-11990	Compacted NaturalGroundSoilInstallation Woks for Landscape	5.00	60%	0%	24 Oct 26	28Oct-26	19 Jan 27	24Jan-27	$4 617 4 75	$000	$80291.25	0.00
	PLANTING	2800	0%	0%	02 Nov-26	03Dec-26	28 Jan 27	02Mar-27	$000	$000	$5 734 62.50	0.00
MLTX02-004CN-12050	Placement of SweetAgricultural Soil (Including Levelling andGrading)	5.00	0%	0%	02 Nov-26	07Nov-26	28 Jan 27	02Feb-27	$000	$000	$1 864 20.00	0.00
MLTX02-004CN-12060	Placement of LawnGroundCover(Rolling and Compacton)	3.00	0%	0%	01 Dec-26	03Dec-26	28 Feb 27	02Mar-27	$000	$000	$1 751 75.00	0.00
MLTX02-004CN-12070	Placement and Fixationof Trees	3.00	0%	0%	28 Nov-26	30Nov-26	24 Feb 27	27Feb-27	$000	$000	$2 118 67.50	0.00
	WALKING/BIKE PATHS	8.00	0%	9589%	05 Dec-26	13Dec-26	19 Aug 26A	02Mar-27	$000	$265048 85	$2 764 12.47	- 158 00
MLTX02-004CN-12000	BikePathPreparationand InstallationWorks	8.00	0%	92%	05 Dec-26	13Dec-26	19 Aug 26A	02Mar-27	$000	$130681 66	$1 420 45.28	- 158 00
MLTX02-004CN-12010	WalkingPath Preparaton and InstallationWorks	8.00	0%	100%	05 Dec-26	13Dec-26	19 Aug 26A	20Oct-26A	$000	$134367 19	$1 363 67.19	-4500
	GENERAL/FURNITURE	16900	1519%	1594%	07 Oct 26	25Jan-27	17 Oct26A	19May-27	$1 131 97 50	$118778 77	$7 451 51.31	-8300
MLTX02-004CN-11970	Stamped Concete Woksfor landScape(IncludingFinishingWorks)	8.00	0%	0%	14 Dec-26	22Dec-26	27 Oct26	04Nov-26	$000	$000	$14040.00	0.00
MLTX02-004CN-12040	TrafficSignsPosts and Poles Installation	7.00	0%	0%	06 Jan 27	13Jan-27	30 Mar27	06Apr-27	$000	$000	$9 750 00	0.00
MLTX02-004CN-12440	Fixationand Installationof Steel Frame for Benches	1200	0%	0%	14 Dec-26	27Dec-26	08 Mar27	20Mar-27	$000	$000	$17276.00	0.00
MLTX02-004CN-12450	Fixationand Installationof Benches	8.00	0%	0%	28 Dec-26	05Jan-27	21 Mar27	29Mar-27	$000	$000	$40310.72	0.00
MLTX02-004CN-12460	Fixationand Installationof PrecastConcrete Seats (Rectangular)	8.00	0%	0%	28 Dec-26	05Jan-27	21 Mar27	29Mar-27	$000	$000	$43680.00	0.00
MLTX02-004CN-12470	Fixationand Installationof PrecastConcrete Seats (Circular)	8.00	0%	0%	28 Dec-26	05Jan-27	21 Mar27	29Mar-27	$000	$000	$17160.00	0.00
MLTX02-004CN-12480	Fixationand Installationof PrecastConcrete Trash Bins	8.00	0%	0%	17 Jan 27	25Jan-27	08 May 27	19May-27	$000	$000	$14625.00	0.00
MLTX02-004CN-12920	Preliminary Woks forSiteLightPoles IncludingCableand Bases Woks	1400	100%	0%	07 Oct 26	22Oct-26	08 Jan 27	18Jan-27	$1 131 97 50	$000	$1 131 97.50	0.00
MLTX02-004CN-12930	Installing ofSiteLightPoles	1100	0%	25%	24 Dec-26	05Jan-27	17 Oct26A	25Mar-27	$000	$118778 77	$4 751 15.00	- 123 00
	PARKING	1200	0%	0%	23 Dec-26	05Jan-27	05 Nov 25	18Nov-26	$000	$000	$97500.48	0.00
MLTX02-004CN-11 940	Interlock Installaton (8 Cm)for ParkingArea(IncludingFinishing Works)	7.00	0%	0%	29 Dec-26	05Jan-27	11 Nov 25	18Nov-26	$000	$000	$68249.02	0.00
MLTX02-004CN-11 950	Site Preparation & CompactionUnderInterlockfor ParkingArea	5.00	0%	0%	23 Dec-26	28Dec-26	05 Nov 25	10Nov-26	$000	$000	$29251.46	0.00
	TOILETSERVICE BULDING	18080	9992%	4689%	14 Jun 26	16Nov-26	14 Jun 26A	11Jan-27	$1279.1061 3	$600213 56	$1 280 1 61 3	-4800
	STRUCTUREWORKS	5680	100%	100%	14 Jun 26	19Aug-26	14 Jun 26A	09Aug-26A	$1 579 50 00	$157950 00	$1 579 50.00	9.00
	CONCRETE WORKS	5080	100%	100%	14 Jun 26	19Aug-26	14 Jun 26A	23Jul-26A	$1 137 82 50	$113782 50	$1 137 82.50	23.00
	SUB-STRUCTURE	1640	100%	100%	14 Jun 26	02Jul-26	14 Jun 26A	02Jul-26A	$33 345 0 00	$33 345 0.00	$33345.00	0.00
MLTX02-004CN-124	Plain Concete Under Footing	1.00	100%	100%	14 Jun 26	15Jun-26	14 Jun 26A	15Jun-26A	$1 170 0 00	$1170.00	$1 170 0 00	0.00
MLTX02-004CN-125	ReinforcedConcrete Woks for Slab onGrade Including Steel Fixing	1560	100%	100%	15 Jun 26	02Jul-26	15 Jun 26A	02Jul-26A	$32 217 5 00	$32 217 5.00	$32175.00	0.00
	SUPER-STRUCTURE	1900	100%	100%	16 Jul-26	19Aug-26	19 Jul-26A	23Jul-26A	$80 437 5 00	$80 437.50	$80437.50	24.00
MLTX02-004CN-125	AAC Panels Works for Walls	1100	100%	100%	16 Jul-26	28Jul-26	19 Jul-26A	21Jul-26A	$48 826 2 50	$48 826 2.50	$48262.50	7.80
MLTX02-004CN-125	Parpet Works and Lintels	8.00	100%	100%	11 Aug-26	19Aug-26	23 Jul-26A	23Jul-26A	$1 608 7 50	$1 608 7.50	$16087.50	7.00
MLTX02-004CN-125	AAC Panels Works for Slabs	1000	100%	100%	29 Jul-26	09Aug-26	21 Jul-26A	22Jul-26A	$1 608 7 50	$1 608 7.50	$16087.50	8.00
	UNDER GROUNDSEPTIC TANK	3870	100%	100%	15 Jun 26	10Aug-26	15 Jun 26A	15Jul-26A	$33 393 0 00	$33 393 0.00	$33930.00	22.40
MLTX02-004CN-13080	Plain Concete Under Footing	1.00	100%	100%	15 Jun 26	16Jun-26	15 Jun 26A	16Jun-26A	$1 170 0 00	$1170.00	$1 170 0 00	0.00
MLTX02-004CN-13090	ReinforcedConcrete Woks for Tank SlabIncludingShutteing and Steel Fixing	1600	100%	100%	23 Jul-26	10Aug-26	11 Jul-26A	15Jul-26A	$8 775 0 00	$8775.00	$8 775 0 00	11.40
MLTX02-004CN-13100	ReinforcedConcrete Woks for Tank FoundationIncludingShutteing and Steel Fixing	1330	100%	100%	16 Jun 26	01Jul-26	15 Jun 26A	01Jul-26A	$7 605 0 00	$7605.00	$7 605 0 00	0.00
MLTX02-004CN-13110	ReinforcedConcrete Woks for Tank Walls hcluding Steel Fixing	1600	100%	100%	05 Jul-26	22Jul-26	05 Jul-26A	07Jul-26A	$1 638 0 00	$1 638 0.00	$16380.00	13.00
	THERMAL& MOISTERPROTECTION	5680	100%	100%	14 Jun 26	19Aug-26	14 Jun 26A	09Aug-26A	$1 023 7 50	$1 023 7.50	$10237.50	9.00
	ANTTERMITCONTROL	1480	100%	100%	14 Jun 26	30Jun-26	14 Jun 26A	30Jun-26A	$4 387 5 00	$4387.50	$4 387 5 00	0.00
MLTX02-004CN-125	AntiTermite Works Under Foundation	1.10	100%	100%	14 Jun 26	15Jun-26	14 Jun 26A	15Jun-26A	$1 755 0 00	$1755.00	$1 755 0 00	0.00
MLTX02-004CN-125	AntiTermite Works Under Slab onGradeand Grade Beams	4.00	100%	100%	27 Jun 26	30Jun-26	27 Jun 26A	30Jun-26A	$2 632 5 00	$2632.50	$2 632 5 00	0.00
	POLYETHYLENESHEET	1480	100%	100%	14 Jun 26	30Jun-26	14 Jun 26A	30Jun-26A	$2 193 7 50	$2193.75	$2 193 7 50	0.00
MLTX02-004CN-125	Water ProofingUnderBlinding Concrete(PolythelenSheet)	1.10	100%	100%	14 Jun 26	15Jun-26	14 Jun 26A	15Jun-26A	$8 775 0	$877.50	$8 775 0	0.00
MLTX02-004CN-125	Water ProofingUnderSlab on Grade (Polythelen Sheet)	2.00	100%	100%	29 Jun 26	30Jun-26	29 Jun 26A	30Jun-26A	$1 316 2 50	$1316.25	$1 316 2 50	0.00
	EPOXY	8.00	100%	100%	11 Aug-26	19Aug-26	08 Aug 26A	09Aug-26A	$3 656 2 50	$3656.25	$3 656 2 50	6.00
MLTX02-004CN-125	Surface Preparaton for Epoxy Coating	3.00	100%	100%	11 Aug-26	13Aug-26	08 Aug 26A	08Aug-26A	$1 096 8 8	$1096.88	$1 096 8 8	2.00
MLTX02-004CN-125	EpoxyCoating forWalls andSlabof Tank	5.00	100%	100%	15 Aug-26	19Aug-26	09 Aug 26A	09Aug-26A	$2 559 3 8	$2559.38	$2 559 3 8	4.00
	MASONARY WORK	5.00	100%	100%	11 Jul-26	15Jul-26	25 Jul-26A	05Aug-26A	$1 228 5 00	$1 228 5.00	$12285.00	-450
MLTX02-004CN-12 600	CMU MasonaryWorksIncluding all Accessories	5.00	100%	100%	11 Jul-26	15Jul-26	25 Jul-26A	05Aug-26A	$1 228 5 00	$1 228 5.00	$12285.00	-450
	THERMAL& MOISTER PROTECTION	1500	100%	9282%	20 Aug-26	13Sep-26	29 Sep 26A	04Nov-26	$3 470 0 25	$2 270 9.09	$34700.25	-1100
MLTX02-004CN-12 650	FinalizeWaterProofing Worksfor Roofingand Wet Areas	8.00	100%	85%	05 Sep-26	13Sep-26	29 Sep 26A	04Nov-26	$1 660 8 15	$1 411 6.93	$16608.15	-2400
MLTX02-004CN-12 620	PreparingSurface andPreliminaryWorksforToilets Waterpoofing	2.00	100%	100%	20 Aug-26	22Aug-26	10 Oct26A	15Oct-26A	$2 106 0 00	$2106.00	$2 106 0 00	-400
MLTX02-004CN-12 630	FinalizeWaterProofing Worksfor Toilets	5.00	100%	100%	23 Aug-26	27Aug-26	10 Oct26A	15Oct-26A	$4 914 0 00	$4914.00	$4 914 0 00	-100
MLTX02-004CN-12 640	PreparingSurface andPreliminaryWorksforRoofing andWet Areas Insulaton	6.00	100%	100%	29 Aug-26	03Sep-26	29 Sep 26A	29Sep-26A	$1 107 2 10	$1 107 2.10	$11072.10	5.00
	MECHANICALWORK	8900	100%	3078%	29 Aug-26	18Oct-26	06 Jul-26A	13Dec-26	$1 332 85 13	$133350 75	$4 332 85.13	-9600
	HVAC SYSTEM	2400	100%	4755%	12 Sep-26	18Oct-26	06 Oct26A	13Dec-26	$2 188 5 00	$1 325 0.00	$27885.00	-2800




Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work

TASK filter: All Activities


© Oracle Corporation

ActivityID	ActivityName	Orginal Duration	Schedule %	Performance% Complete	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Variance - BL Project
MLTX02-004CN-12730	Installand FinishHVAC and VentilationWorksIncludingSplitAir Units	9.00	100%	0%	08 Oct 26	18Oct-26	03 Dec 25	13Dec-26	$1,462,500	$000	$14625.00	0.00
MLTX02-004CN-12720	Preliminary HVAC and Ventilation Works	4.00	100%	100%	12 Sep-26	15Sep-26	05 Oct 26A	08Oct-26A	$9,360.00	$9360.00	$9,360.00	1.00
MLTX02-004CN-12740	Exhaust, Air Ducts Installationwithall Accessories	8.00	100%	100%	16 Sep-26	26Sep-26	10 Oct 26A	12Oct-26A	$3,900.00	$3900.00	$3,900.00	5.00
WATERSUPPLYSYSTEM		8000	100%	4291%	31 Aug-26	10Oct-26	04 Aug 26 A	05Dec-26	$2,524,275.00	$1083225.00	$2,524,275.00	-7100
MLTX02-004CN-12770	Installing ofBooster PumpUnitsIncluding fittings and accessories	5.00	100%	0%	27 Sep-26	01Oct-26	08 Nov 25	12Nov-26	$91,000.00	$000	$91000.00	0.00
MLTX02-004CN-13170	Installing ofValvesand Fittings	6.00	100%	0%	03 Sep-26	09Sep-26	27 Oct 26	02Nov-26	$9,750.00	$000	$9,750.00	0.00
MLTX02-004CN-13260	Installing ofWater Heater	7.00	100%	0%	03 Oct 26	10Oct-26	28 Nov 25	05Dec-26	$1,755.00	$000	$1,755.00	0.00
MLTX02-004CN-12780	Installing ofGRP Tanks	8.00	100%	60%	16 Sep-26	26Sep-26	15 Sep 26 A	07Nov-26	$1,040,000.00	$624,000.00	$1,040,000.00	-3700
MLTX02-004CN-12750	Installing ofPPR Pipes andFittings for WaterNetwork	3.00	100%	100%	31 Aug-26	02Sep-26	04 Aug 26 A	08Aug-26A	$6,922.50	$6922.50	$6,922.50	-055
MLTX02-004CN-12760	Installing ofHDPE Pipes andValvesforWaterSupplyNetwok	3.00	100%	100%	10 Sep-26	13Sep-26	05 Oct 26A	10Oct-26A	$3,900.00	$3900.00	$39000.00	-200
SEWERDRAIN AGESYSTEM		8400	100%	7.79%	29 Aug-26	12Oct-26	04 Jul -26A	07Dec-26	$1,510,226.63	$1,176,825.00	$1,510,226.63	-9600
MLTX02-004CN-12800	Installing ofPlumping Fixturesand Accessories	2.00	100%	0%	17 Sep-26	19Sep-26	14 Nov 25	15Nov-26	$1,035,938.00	$000	$10359.38	0.00
MLTX02-004CN-13180	Installing UPVC Pipes for ExternalConnecton for Sewage Network	7.00	100%	0%	09 Sep-26	16Sep-26	05 Nov 25	12Nov-26	$8,531,250	$000	$85312.50	0.00
MLTX02-004CN-13250	Installing Inspection Chamber forSewageNetwok	8.00	100%	0%	31 Aug-26	08Sep-26	27 Oct 26	04Nov-26	$12,187,500	$000	$12187.50	0.00
MLTX02-004CN-13270	Installing ofToilet Fixturesand Accessories Such as Closetsand Basins	9.00	100%	0%	03 Oct 26	12Oct-26	28 Nov 25	07Dec-26	$3,139,500	$000	$31395.00	0.00
MLTX02-004CN-12790	Installing UPVC Pipes for Sewage Network	2.00	100%	100%	29 Aug-26	30Aug-26	04 Jul -26A	08Aug-26A	$1,176,825	$1,176,825	$11768.25	-2820
FIREPROTECTION		7.00	100%	0%	11 Oct 26	18Oct-26	06 Dec 25	13Dec-26	$1,950.00	$000	$1,950.00	0.00
MLTX02-004CN-12810	Installing ofFireFighting Extinguisherand accessories (PIE-1, PIE-2)	7.00	100%	0%	11 Oct 26	18Oct-26	06 Dec 25	13Dec-26	$1,950.00	$000	$1,950.00	0.00
ELECTRICALWORKS		11700	100%	4943%	20 Aug-26	24Oct-26	11 Aug 25 A	19Dec-26	$3,765,262.50	$1861287.50	$3,765,262.50	-5600
ROUGH-N WORKS		2500	100%	100%	20 Aug-26	30Aug-26	11 Aug 25 A	26Aug-26A	$1,488,825.00	$1488825.00	$1,488,825.00	-500
MLTX02-004CN-12830	Preliminary Woks forPanelBoards	9.00	100%	100%	20 Aug-26	30Aug-26	11 Aug 25 A	26Aug-26A	$76,650.00	$76,650.00	$76,650.00	-500
MLTX02-004CN-12850	Preliminary Woks forCableWorks	9.00	100%	100%	20 Aug-26	30Aug-26	11 Aug 25 A	26Aug-26A	$107,000.00	$107,000.00	$107,000.00	-500
MLTX02-004CN-12860	Preliminary Woks forSockets andPowerPoints	9.00	100%	100%	20 Aug-26	30Aug-26	11 Aug 25 A	26Aug-26A	$92,309.91	$92309.91	$92,309.91	-500
MLTX02-004CN-12880	Preliminary Woks forLightningWorks	9.00	100%	100%	20 Aug-26	30Aug-26	11 Aug 25 A	26Aug-26A	$97,500.00	$9750.00	$97,500.00	-500
MLTX02-004CN-12900	Preliminary Woks forData& TelecommunicationSystem	9.00	100%	100%	20 Aug-26	30Aug-26	11 Aug 25 A	26Aug-26A	$122,850.00	$122850.00	$122,850.00	-500
MLTX02-004CN-12940	Preliminary Woks forSecurity and Access Control System	9.00	100%	100%	20 Aug-26	30Aug-26	11 Aug 25 A	26Aug-26A	$152,665.50	$152,665.50	$152,665.50	-500
MLTX02-004CN-13230	Preliminary Woks forEarthing Works	9.00	100%	100%	20 Aug-26	30Aug-26	11 Aug 25 A	26Aug-26A	$156,000.00	$156,000.00	$156,000.00	-500
FIXTURE WORKS		2100	100%	1636%	08 Oct 26	24Oct-26	06 Oct 26 A	19Dec-26	$2,276,437.50	$372,163.37	$2,276,437.50	-5000
MLTX02-004CN-12820	Installing ofFireautomationand Fire Alarm System	5.00	100%	0%	19 Oct 26	24Oct-26	14 Dec 25	19Dec-26	$343,200.00	$000	$34320.00	0.00
MLTX02-004CN-12840	Installing andFinish Woks ofPanelBoards	1000	100%	0%	08 Oct 26	19Oct-26	03 Dec 25	14Dec-26	$840,750.00	$000	$84075.00	0.00
MLTX02-004CN-12890	Installing andFinalize Worksof Lighting Woks includingLightFixtures	7.00	100%	0%	11 Oct 26	18Oct-26	06 Dec 25	13Dec-26	$160,500.00	$000	$160500.00	0.00
MLTX02-004CN-12910	Installing Data andTelecommunicaton System with allAccessories	7.00	100%	0%	11 Oct 26	18Oct-26	06 Dec 25	13Dec-26	$184,275.00	$000	$18427.50	0.00
MLTX02-004CN-12950	Installing andFinalize Worksof Securityand Access ControlSystem	9.00	100%	0%	08 Oct 26	18Oct-26	03 Dec 25	13Dec-26	$228,998.63	$000	$22899.83	0.00
MLTX02-004CN-12970	Installing andFinalize Worksof Lightning Protection System	9.00	100%	0%	08 Oct 26	18Oct-26	03 Dec 25	13Dec-26	$146,250.00	$000	$14625.00	0.00
MLTX02-004CN-12870	Installing andFinalize Worksof Sockets and PowerPoints	7.00	100%	100%	11 Oct 26	18Oct-26	08 Oct 26 A	10Oct-26A	$138,466.37	$138466.37	$138,466.37	5.00
MLTX02-004CN-12960	Installing andFinalize Worksof EarthingWorks	9.00	100%	100%	08 Oct 26	18Oct-26	06 Oct 26 A	10Oct-26A	$234,000.00	$234000.00	$234,000.00	5.00
DOORS/WINDOWS		3900	100%	1429%	20 Aug-26	13Oct-26	18 Oct 26 A	08Dec-26	$682,500.00	$97500.00	$682,500.00	1.00
MLTX02-004CN-13040	FinalizeGlazzedCurtain Wall Works	5.00	100%	0%	08 Oct 26	13Oct-26	03 Dec 25	08Dec-26	$351,000.00	$000	$35100.00	0.00
MLTX02-004CN-13120	Preliminay Woks ForWindows/CutainWall	1200	100%	0%	20 Aug-26	02Sep-26	27 Oct 26	09Nov-26	$234,000.00	$000	$23400.00	0.00
MLTX02-004CN-12660	Preliminay Woks ForDoors	1000	100%	100%	20 Aug-26	31Aug-26	18 Oct 26 A	20Oct-26A	$39,000.00	$3900.00	$39,000.00	7.00
MLTX02-004CN-12670	FinalizeMetalDoorsfor Toilets Building	5.00	100%	100%	08 Oct 26	13Oct-26	20 Oct 26 A	22Oct-26A	$58,500.00	$5850.00	$58,500.00	2.00
METALWORKS		2500	100%	0%	20 Aug-26	04Oct-26	27 Oct 26	24Nov-26	$136,500.00	$000	$136500.00	13.00
MLTX02-004CN-12610	Installationof GalvanizedSteelLadder	5.00	100%	0%	16 Sep-26	21Sep-26	08 Nov 25	12Nov-26	$58,500.00	$000	$58,500.00	0.00
MLTX02-004CN-12980	Installationof DICoverfor Tank	4.00	100%	0%	20 Aug-26	24Aug-26	27 Oct 26	31Oct-26	$39,000.00	$000	$39,000.00	0.00
MLTX02-004CN-12990	Installationof GalvanizedSteelRoofScupper	1000	100%	0%	22 Sep-26	04Oct-26	14 Nov 25	24Nov-26	$39,000.00	$000	$39,000.00	0.00
FINISHING WORKS		10200	9927%	4743%	29 Aug-26	16Nov-26	05 Sep 25 A	11Jan-27	$1,436,615.00	$682,990.00	$1,436,615.00	-4200
FLOORFINISHES		6600	9386%	6932%	03 Sep-26	16Nov-26	08 Oct 26 A	11Jan-27	$1,610,700.00	$1,116,750.00	$1716000.00	-1900
MLTX02-004CN-13050	Granite TilesFloorFinish Woks	6.00	100%	0%	06 Sep-26	12Sep-26	27 Oct 26	02Nov-26	$292,500.00	$000	$292,500.00	0.00
MLTX02-004CN-13060	EpoxyCoaton Concete Floor	2000	10%	0%	25 Oct 26	16Nov-26	20 Dec 25	11Jan-27	$117,000	$000	$117,000.00	0.00
MLTX02-004CN-13070	Ceramic SkirtingTiles Finish Woks	4.00	100%	0%	13 Sep-26	16Sep-26	03 Nov 25	07Nov-26	$117,000.00	$000	$117,000.00	0.00
MLTX02-004CN-12680	Ceramic Tiles Floor FinishWorks	2.00	100%	100%	03 Sep-26	05Sep-26	08 Oct 26 A	12Oct-26A	$119,500.00	$119,500.00	$119,500.00	-200
WALLFINISHES		7000	100%	4355%	29 Aug-26	10Oct-26	05 Sep 25 A	05Dec-26	$1,141,725.00	$497,185.00	$1,141,725.00	-4200
MLTX02-004CN-13010	PaintingFinishWorks forExtenal Walls	3.00	100%	0%	14 Sep-26	16Sep-26	27 Oct 26	29Oct-26	$104,780.00	$000	$104,780.00	0.00
MLTX02-004CN-13030	Phendic Patitions for Toilets	7.00	100%	0%	24 Sep-26	01Oct-26	19 Nov 25	26Nov-26	$312,000.00	$000	$312,000.00	0.00
MLTX02-004CN-13140	Glass Partitions includingallaccessoriesand doors	5.00	100%	0%	03 Oct 26	07Oct-26	28 Nov 25	02Dec-26	$122,850.00	$000	$122,850.00	0.00
MLTX02-004CN-13150	Granite Cappingfor Paapet	2.00	100%	0%	14 Sep-26	15Sep-26	05 Nov 25	07Nov-26	$81,510.00	$000	$81,510.00	0.00
MLTX02-004CN-13240	PaintingFinishWorks forIntenalWalls	2.00	100%	0%	08 Oct 26	10Oct-26	03 Dec 25	05Dec-26	$23,400.00	$000	$23,400.00	0.00
MLTX02-004CN-12690	Preliminay Woks for Wall Finish Worksincluding Plasteing (Intenal)	3.00	100%	100%	31 Aug-26	02Sep-26	05 Sep 25 A	12Sep-26A	$183,690.00	$183,690.00	$183,690.00	-400
MLTX02-004CN-13000	Preliminay Woks for Wall Finish Works(External)	1400	100%	100%	29 Aug-26	13Sep-26	20 Sep 26 A	30Sep-26A	$65,520.00	$6552.00	$65,520.00	5.00
MLTX02-004CN-13020	Ceramic Finish Worksfor Walls	5.00	100%	100%	06 Sep-26	10Sep-26	04 Oct 26 A	06Oct-26A	$156,975.00	$156,975.00	$156,975.00	2.00
MLTX02-004CN-13130	Stone Cladding FinishWorksforExternal Walls	5.00	100%	100%	17 Sep-26	22Sep-26	10 Oct 26A	15Oct-26A	$91,000.00	$9100.00	$91,000.00	-100
CELLING FINISHES		2900	100%	5254%	03 Sep-26	01Oct-26	19 Oct 26 A	23Nov-26	$131,820.00	$69,264.00	$131,820.00	-700
MLTX02-004CN-13280	PaintingFinishWorks forCeiling	9.00	100%	0%	21 Sep-26	01Oct-26	14 Nov 25	23Nov-26	$16,380.00	$000	$16,380.00	0.00
MLTX02-004CN-13300	Preliminay Woks for Ceiling Painting Woks	1500	100%	0%	03 Sep-26	20Sep-26	27 Oct 26	12Nov-26	$41,670.60	$000	$41,670.60	0.00
MLTX02-004CN-13290	Gypsum BoardSuspended Ceiling finishWorksForCeiling	4.00	100%	100%	16 Sep-26	20Sep-26	19 Oct 26 A	21Oct-26A	$69,264.00	$69264.00	$69,264.00	1.00
SPECIALTIES WORK		1200	100%	0%	20 Sep-26	04Oct-26	16 Nov 25	29Nov-26	$39,000.00	$000	$39000.00	0.00
MLTX02-004CN-12700	SanitaryFixtures andAccessoriesWorks	3.00	100%	0%	20 Sep-26	22Sep-26	16 Nov 25	18Nov-26	$14,625.00	$000	$14625.00	0.00
MLTX02-004CN-13150	Installationof PhenolicLocker	2.00	100%	0%	03 Oct 26	04Oct-26	28 Nov 25	29Nov-26	$24,375.00	$000	$24375.00	0.00
TESTING & COMMISSIONING		6300	0%	0%	17 Nov-26	19Jan-27	28 Jan 27	15Apr-27	$000	$000	$0.00	-800
MLTX02-0047C-11890	Testing and Commissioning forMEP Woks for PlaygroundArea	1600	0%	0%	27 Dec-26	13Jan-27	29 Mar27	15Apr-27	$000	$000	$0.00	0.00
MLTX02-0047C-11900	Testing and Commissioning forMEP Woks for ToiletServiceBuilding	2500	0%	0%	17 Nov-26	15Dec-26	28 Jan 27	27Feb-27	$000	$000	$0.00	0.00

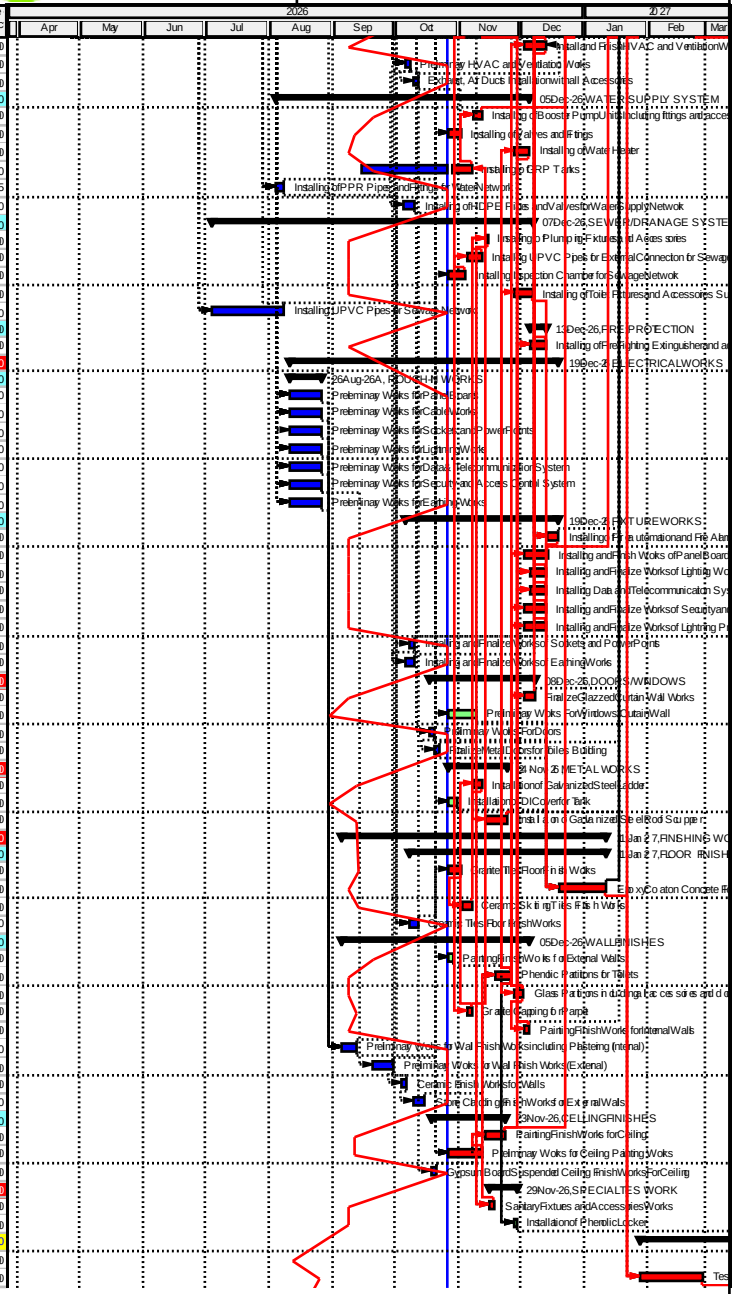

© Oracle Corporation

ActivityID	ActivityName	Orginal Duration	Schedule %	Performance% Complete	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Variance - BL Project
MLTX02-004TC-11910	Testing and Commissioning forMEP Works for LandscapeWorks	5.00	0%	0%	14-Jan-27	19-Jan-27	07-Apr-27	12-Apr-27	$000	$000	$0.00	0.00
PROJECT CLOSEOUT & DEMOBILIZATION		28.00	0%	0%	14-Jan-27	25-Jan-27	29-Mar-27	29-Apr-27	$000	$000	$0.00	-18.00
As-Built DWGs		26.00	0%	0%	14-Jan-27	23-Jan-27	29-Mar-27	27-Apr-27	$000	$000	$0.00	-18.00
As-BuiltDWGs Submittals		22.00	0%	0%	14-Jan-27	18-Jan-27	29-Mar-27	22-Apr-27	$000	$000	$0.00	-18.00
MLTX02-004CO-12000	As-BuiltDWGs SubmittalforPlaygound Aea Works	4.00	0%	0%	14-Jan-27	18-Jan-27	19-Apr-27	22-Apr-27	$000	$000	$0.00	0.00
MLTX02-004CO-12010	As-BuiltDWGs Submittal forToilet/ServiceBuilding Works	4.00	0%	0%	14-Jan-27	18-Jan-27	29-Mar-27	01-Apr-27	$000	$000	$0.00	0.00
MLTX02-004CO-12020	As-BuiltDWGs SubmittalforLandscape Works	4.00	0%	0%	14-Jan-27	18-Jan-27	07-Apr-27	11-Apr-27	$000	$000	$0.00	0.00
As-BuiltDWGs Approvals		22.00	0%	0%	19-Jan-27	23-Jan-27	01-Apr-27	27-Apr-27	$000	$000	$0.00	-18.00
MLTX02-004CO-12040	As-BuiltDWGs AgprovalforPlaygound Aea Works	4.00	0%	0%	19-Jan-27	23-Jan-27	21-Apr-27	27-Apr-27	$000	$000	$0.00	0.00
MLTX02-004CO-12050	As-BuiltDWGs AppovalforToiletService BuildingWorks	4.00	0%	0%	19-Jan-27	23-Jan-27	01-Apr-27	06-Apr-27	$000	$000	$0.00	0.00
MLTX02-004CO-12060	As-BuiltDWGs AppovalforlandscapeWorks	4.00	0%	0%	19-Jan-27	23-Jan-27	12-Apr-27	15-Apr-27	$000	$000	$0.00	0.00
Demobilizatbn		6.00	0%	0%	19-Jan-27	25-Jan-27	21-Apr-27	29-Apr-27	$000	$000	$0.00	0.00
MLTX02-004CO-12080	Demobilizaton ol Manpower	2.00	0%	0%	19-Jan-27	20-Jan-27	21-Apr-27	25-Apr-27	$000	$000	$0.00	0.00
MLTX02-004CO-12090	RemovalofEquipment fom Site	2.00	0%	0%	19-Jan-27	20-Jan-27	21-Apr-27	25-Apr-27	$000	$000	$0.00	0.00
MLTX02-004CO-12100	Site CleanUp	2.00	0%	0%	21-Jan-27	23-Jan-27	26-Apr-27	27-Apr-27	$000	$000	$0.00	0.00
MLTX02-004CO-12110	RestbrationofGroundSurfaces	2.00	0%	0%	24-Jan-27	25-Jan-27	28-Apr-27	29-Apr-27	$000	$000	$0.00	0.00

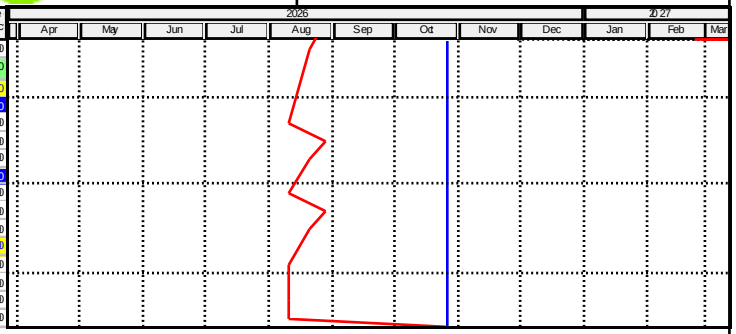

© Oracle Corporation
