
MLTX-02-004 - Playground Initiative for Western Region (Asir-Jazan -Jeddah)

Remaining work
D.D 26-10-2026

Activity ID	Activity Name	Original Duration	Schedule %	Performance % Complete	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Variance - BL Project
MLTX-02-004 - Playground hitiative for Western Region (Asir- Jazan - Jeddah) - Update26-10-2026		180.00	2581%	1406%	05Jul-26	25Jan-27	20Apr-26A	19May-27	$ 630,617.02	$347,486.43	$124525.478.83	-155.00
KEY MILE STONES		165.00	0%	0%	22Jul-26	25Jan-27	27Oct-26	19May-27	$000	$000	$000	-100
GENERAL MILESTONES		0 00	0%	0%	25Jan-27	25Jan-27	19May-27	19May-27	$000	$000	$000	0.00
MLTX02-004-MS-1080	Project Completion	0 00	0%	0%		25Jan-27		19May-27	$000	$000	$000	0.00
CONTRACTUALMILESTONE		165.00	0%	0%	22Jul-26	25Jan-27	27Oct-26	19May-27	$000	$000	$000	-100
MLTX02-004-MS-1160	Completionof Asir Works	0 00	0%	0%		19Jan-27		05Apr-27	$000	$000	$000	0.00
MLTX02-004-MS-1170	Completionof Jazan Works	0 00	0%	0%		25Jan-27		19May-27	$000	$000	$000	0.00
MLTX02-004-MS-1180	Completionof Jeddah Works	0 00	0%	0%		25Jan-27		01Apr-27	$000	$000	$000	0.00
MLTX02-004-MS-1100	Completionof Engineering	0 00	100%	0%		22Jul-26		12Nov-26	$000	$000	$000	0.00
MLTX02-004-MS-1120	Completionof LevellingWorks	0 00	100%	0%		09Aug-26		27Oct-26	$000	$000	$000	0.00
MLTX02-004-MS-1070	Completionof Testing &Commissioning	0 00	0%	0%		19Jan-27		18Apr-27	$000	$000	$000	0.00
MLTX02-004-MS-1130	Completionof Toilet Building	0 00	0%	0%		30Nov-26		11Jan-27	$000	$000	$000	0.00
MLTX02-004-MS-1140	Completionof Playgrourd Area	0 00	0%	0%		16Jan-27		06May-27	$000	$000	$000	0.00
MLTX02-004-MS-1150	Completionof Natural Landscape Works	0 00	0%	0%		13Dec-26		18Mar-27	$000	$000	$000	0.00
JEDD AH		140.00	3793%	181%	05Jul-26	25Jan-27	20Apr-26A	01Apr-27	$3288,900.98	$ 156 9 602 66	$8669,997.04	-115.00
ENGINEERING		1500	0%	0%	05Jul-26	21Jul-26	27Oct-26	12Nov-26	$000	$000	$000	0.00
METHOD STATEMENTS		1500	0%	0%	05Jul-26	21Jul-26	27Oct-26	12Nov-26	$000	$000	$000	0.00
METHOD STATEMENT SUBMITTAL		5 00	0%	0%	05Jul-26	09Jul-26	27Oct-26	01Nov-26	$000	$000	$000	0.00
ARCHITECTURE WORKS		5 00	0%	0%	05Jul-26	09Jul-26	27Oct-26	01Nov-26	$000	$000	$000	0.00
ML TX0 2-004 EN 12330	Preparation & Submission of Method Statement for Fence Works	5 00	100%	0%	05Jul-26	09Jul-26	27Oct-26	01Nov-26	$000	$000	$000	0.00
METHOD STATEMENT APPROVAL		1000	0%	0%	11Jul-26	21Jul-26	02Nov-26	12Nov-26	$000	$000	$000	0.00
ARCHITECTURE WORKS		1000	0%	0%	11Jul-26	21Jul-26	02Nov-26	12Nov-26	$000	$000	$000	0.00
ML TX0 2-004 EN 15390	Approvalof Method Statement for Fence Works	1000	100%	0%	11Jul-26	21Jul-26	02Nov-26	12Nov-26	$000	$000	$000	0.00
PREQUALIFICATION & MATERIAL		1000	0%	0%	05Jul-26	15Jul-26	27Oct-26	07Nov-26	$000	$000	$000	0.00
MATERIAL SUBMITTAL		1000	0%	0%	05Jul-26	15Jul-26	27Oct-26	07Nov-26	$000	$000	$000	0.00
PLAYGROUND WORKS		1000	0%	0%	05Jul-26	15Jul-26	27Oct-26	07Nov-26	$000	$000	$000	0.00
STEEL TENSIONCABLES		1000	0%	0%	05Jul-26	15Jul-26	27Oct-26	07Nov-26	$000	$000	$000	0.00
MLTX02-004-EN-14150	Material Approvalfor Steel TensionCables	1000	100%	0%	05Jul-26	15Jul-26	27Oct-26	07Nov-26	$000	$000	$000	0.00
PRESSURE UNITS		1000	0%	0%	05Jul-26	15Jul-26	27Oct-26	07Nov-26	$000	$000	$000	0.00
MLTX02-004-EN-14170	Material Approvalfor PressureUnits	1000	100%	0%	05Jul-26	15Jul-26	27Oct-26	07Nov-26	$000	$000	$000	0.00
PROCUREMENT		5400	0%	0%	05Jul-26	25Aug-26	20Apr-26A	17Dec-26	$000	$000	$000	-155.00
SHORT LEAD ITEM		4700	0%	0%	05Jul-26	17Aug-26	20Apr-26A	09Dec-26	$000	$000	$000	-155.00
TOILET/SERVICEWORKS		2000	0%	0%	05Jul-26	27Jul-26	27Oct-26	18Nov-26	$000	$000	$000	0.00
PACKAGEAC UNITS		1500	0%	0%	05Jul-26	21Jul-26	27Oct-26	12Nov-26	$000	$000	$000	0.00
ML TX0 2-004 PR 11460	Material Deliveryfor PackageAC Units	1500	100%	0%	05Jul-26	21Jul-26	27Oct-26	12Nov-26	$000	$000	$000	0.00
LIGHTINGFIXTURES		1000	0%	0%	05Jul-26	15Jul-26	27Oct-26	07Nov-26	$000	$000	$000	0.00
ML TX0 2-004 PR 11380	Material Deliveryfor LightingFixtures	1000	100%	0%	05Jul-26	15Jul-26	27Oct-26	07Nov-26	$000	$000	$000	0.00
DISTRIBUTION PANNELS		2000	0%	0%	05Jul-26	27Jul-26	27Oct-26	18Nov-26	$000	$000	$000	0.00
ML TX0 2-004 PR 11210	POfor Distribution Panels	5 00	100%	0%	05Jul-26	09Jul-26	27Oct-26	01Nov-26	$000	$000	$000	0.00
ML TX0 2-004 PR 11220	Material Deliveryfor Distribution Panels	1500	100%	0%	11Jul-26	27Jul-26	02Nov-26	18Nov-26	$000	$000	$000	0.00
FURNITURES		2000	0%	0%	05Jul-26	27Jul-26	27Oct-26	18Nov-26	$000	$000	$000	0.00
ML TX0 2-004 PR 11420	Material Deliveryfor Furnitures	2000	100%	0%	05Jul-26	27Jul-26	27Oct-26	18Nov-26	$000	$000	$000	0.00
PLAYGROUND WORKS		3800	0%	0%	05Jul-26	17Aug-26	27Oct-26	09Dec-26	$000	$000	$000	0.00
PVCMEMBRANE		2000	0%	0%	05Jul-26	27Jul-26	27Oct-26	18Nov-26	$000	$000	$000	0.00
ML TX0 2-004 PR 11620	Material Deliveryfor PVCMembrane	2000	100%	0%	05Jul-26	27Jul-26	27Oct-26	18Nov-26	$000	$000	$000	0.00
ARTIFICIAL TURF		1200	0%	0%	05Jul-26	18Jul-26	27Oct-26	09Nov-26	$000	$000	$000	0.00
ML TX0 2-004 PR 11850	Material Deliveryfor ArtificialTURF	1200	100%	0%	05Jul-26	18Jul-26	27Oct-26	09Nov-26	$000	$000	$000	0.00
RUBBER GRANULES		1200	0%	0%	05Jul-26	18Jul-26	27Oct-26	09Nov-26	$000	$000	$000	0.00
ML TX0 2-004 PR 11880	Material Deliveryfor Rubber Granules	1200	100%	0%	05Jul-26	18Jul-26	27Oct-26	09Nov-26	$000	$000	$000	0.00
PADEL GLASS		1800	0%	0%	05Jul-26	25Jul-26	27Oct-26	16Nov-26	$000	$000	$000	0.00
ML TX0 2-004 PR 11900	Material Deliveryfor Padel Glass	1800	100%	0%	05Jul-26	25Jul-26	27Oct-26	16Nov-26	$000	$000	$000	0.00
PADEL WIREMESH/STEELSETS		1500	0%	0%	05Jul-26	21Jul-26	27Oct-26	12Nov-26	$000	$000	$000	0.00
ML TX0 2-004 PR 11920	Material Deliveryfor WireMesh/Steel Sets	1500	100%	0%	05Jul-26	21Jul-26	27Oct-26	12Nov-26	$000	$000	$000	0.00
MARKING PAINT		1700	0%	0%	29Jul-26	17Aug-26	21Nov-26	09Dec-26	$000	$000	$000	0.00
ML TX0 2-004 PR 11440	Material Deliveryfor Marking Paint	1700	100%	0%	29Jul-26	17Aug-26	21Nov-26	09Dec-26	$000	$000	$000	0.00
PACKAGEAC UNITS		1500	0%	0%	05Jul-26	21Jul-26	27Oct-26	12Nov-26	$000	$000	$000	0.00
ML TX0 2-004 PR 11540	Material Deliveryfor PackageAC Units	1500	100%	0%	05Jul-26	21Jul-26	27Oct-26	12Nov-26	$000	$000	$000	0.00
DISTRIBUTION BOARDS		1500	0%	0%	28Jul-26	13Aug-26	27Oct-26	12Nov-26	$000	$000	$000	0.00
ML TX0 2-004 PR 11720	Material Deliveryfor Distribution Boards	1500	100%	0%	28Jul-26	13Aug-26	27Oct-26	12Nov-26	$000	$000	$000	0.00
LIGHT FIXTURES		1600	0%	0%	05Jul-26	22Jul-26	27Oct-26	14Nov-26	$000	$000	$000	0.00
ML TX0 2-004 PR 11750	Material Deliveryfor Light Fixtures	1600	100%	0%	05Jul-26	22Jul-26	27Oct-26	14Nov-26	$000	$000	$000	0.00
CCTV MATERIALS		2100	0%	0%	05Jul-26	28Jul-26	27Oct-26	19Nov-26	$000	$000	$000	0.00
ML TX0 2-004 PR 11770	POfor CCTV	6 00	100%	0%	05Jul-26	11Jul-26	27Oct-26	02Nov-26	$000	$000	$000	0.00
ML TX0 2-004 PR 11760	Material Deliveryfor CCTV	1500	100%	0%	12Jul-26	28Jul-26	03Nov-26	19Nov-26	$000	$000	$000	0.00
POWER OUTLETS/SWITCHES		1600	0%	0%	05Jul-26	28Jul-26	27Oct-26	14Nov-26	$000	$000	$000	5.00
ML TX0 2-004 PR 11790	POfor Power Outlets/Switches	6 00	100%	0%	05Jul-26	11Jul-26	27Oct-26	02Nov-26	$000	$000	$000	0.00
ML TX0 2-004 PR 11800	Material Deliveryfor Power Outlets/Switches	6 00	100%	0%	22Jul-26	28Jul-26	08Nov-26	14Nov-26	$000	$000	$000	0.00
LANDSCAPE WORKS		3600	0%	0%	05Jul-26	10Aug-26	20Apr-26A	26Nov-26	$000	$000	$000	-155.00
INTERLOCKING PAVING		1200	0%	0%	05Jul-26	18Jul-26	20Apr-26A	27Oct-26	$000	$000	$000	-147.00
ML TX0 2-004 PR 11840	Material Deliveryfor Interlocking Block Pavers	1200	100%	100%	05Jul-26	18Jul-26	20Apr-26A	27Oct-26	$000	$000	$000	-147.00
PAVEMENTMARKING		1000	0%	0%	11Jul-26	21Jul-26	27Oct-26	07Nov-26	$000	$000	$000	0.00
ML TX0 2-004 PR 11330	Material Deliveryfor PavementMarkings	1000	100%	0%	11Jul-26	21Jul-26	27Oct-26	07Nov-26	$000	$000	$000	0.00
TRAFFIC SIGNS		1000	0%	0%	11Jul-26	21Jul-26	27Oct-26	07Nov-26	$000	$000	$000	0.00
ML TX0 2-004 PR 11350	Material Deliveryfor Traffic Signs	1000	100%	0%	11Jul-26	21Jul-26	27Oct-26	07Nov-26	$000	$000	$000	0.00
AGRICULTURE SOIL		1200	0%	0%	11Jul-26	23Jul-26	27Oct-26	09Nov-26	$000	$000	$000	0.00
ML TX0 2-004 PR 11940	Material Deliveryfor Agriculture Soil	1200	100%	0%	11Jul-26	23Jul-26	27Oct-26	09Nov-26	$000	$000	$000	0.00
TRACK SURFACE		1000	0%	0%	05Jul-26	15Jul-26	27Oct-26	07Nov-26	$000	$000	$000	0.00
ML TX0 2-004 PR 11950	Material Deliveryfor Track Surface	1000	100%	0%	05Jul-26	15Jul-26	27Oct-26	07Nov-26	$000	$000	$000	0.00
GRASS/TREES		1500	0%	0%	25Jul-26	10Aug-26	10Nov-26	26Nov-26	$000	$000	$000	0.00
ML TX0 2-004 PR 12000	Material Deliveryfor Grass/Trees	1500	100%	0%	25Jul-26	10Aug-26	10Nov-26	26Nov-26	$000	$000	$000	0.00
LONG LEAD ITEM		4500	0%	0%	05Jul-26	25Aug-26	27Oct-26	17Dec-26	$000	$000	$000	0.00
PLAYGROUND WORKS		4500	0%	0%	05Jul-26	25Aug-26	27Oct-26	17Dec-26	$000	$000	$000	0.00
STEEL TENSIONCABLES		3400	0%	0%	05Jul-26	18Aug-26	27Oct-26	05Dec-26	$000	$000	$000	5.00
ML TX0 2-004 PR 12050	Staging time	7 00	100%	0%	11Aug-26	18Aug-26	28Nov-26	05Dec-26	$000	$000	$000	0.00
ML TX0 2-004 PR 11680	Material Deliveryfor Steel Tension Cables	1500	100%	0%	16Jul-26	02Aug-26	08Nov-26	24Nov-26	$000	$000	$000	0.00

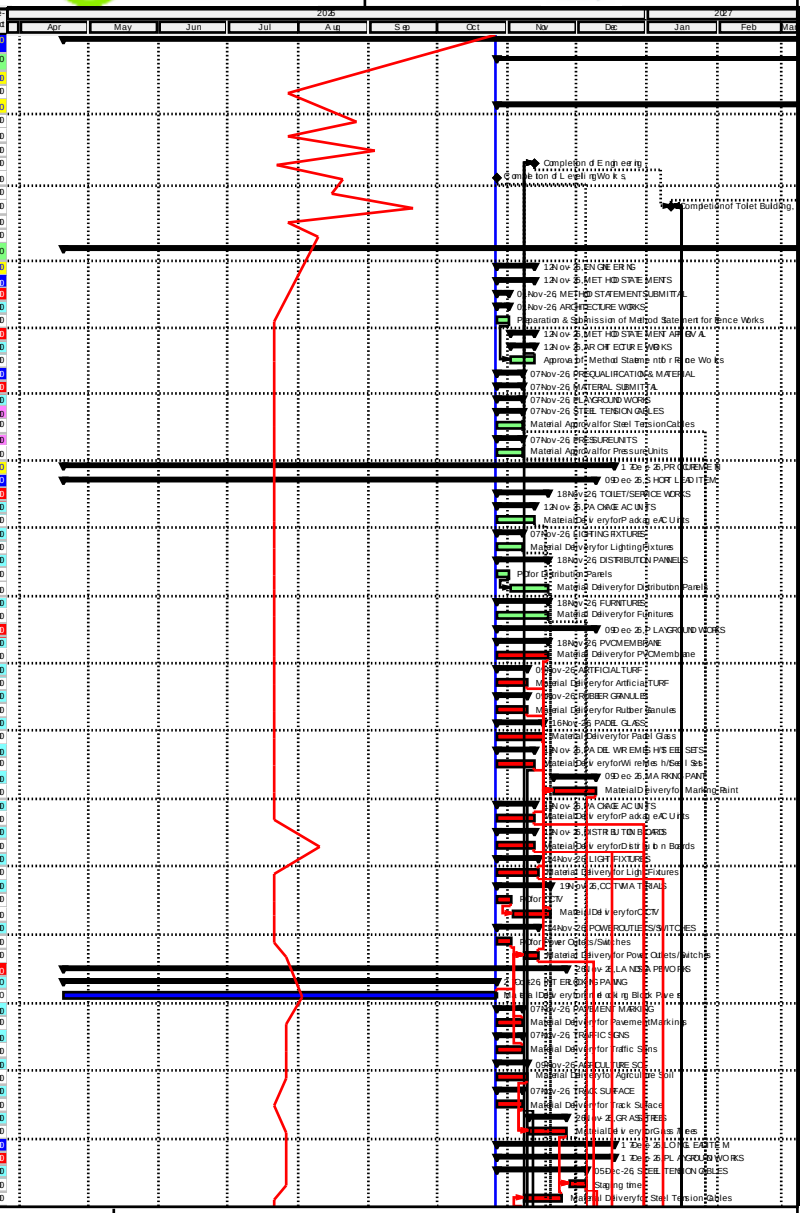

Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work

TASK filter: Remaining work

© Oracle Corporation

MLTX-02-004 - Playground Initiative for Western Region (Asir-Jazan -Jeddah)

Remaining work
D.D 26-10-2026

Activity ID	Activity Name	Original Duration	Schedule %	Performance % Complete	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Variance - BL Project
ML TX02-004-PR-12010	Material Fabrication for Steel Tension Cables	1000	100%	0%	05-Jul-26	15-Jul-26	27-Oct-26	07-Nov-26	$000	$000	$000	0.00
EMERGENCY DOORS		4000	0%	0%	05-Jul-26	19-Aug-26	27-Oct-26	12-Dec-26	$000	$000	$000	0.00
ML TX02-004-PR-12050	Staging time	5.00	100%	0%	15-Aug-26	19-Aug-26	07-Dec-26	12-Dec-26	$000	$000	$000	0.00
ML TX02-004-PR-11650	Material Delivery for Emegency Doors	2000	100%	0%	22-Jul-26	13-Aug-26	14-Nov-26	06-Dec-26	$000	$000	$000	0.00
ML TX02-004-PR-12020	Material Fabrication for Emergency Doors	1500	100%	0%	05-Jul-26	21-Jul-26	27-Oct-26	12-Nov-26	$000	$000	$000	0.00
PRESSURE UNITS		4500	0%	0%	05-Jul-26	25-Aug-26	27-Oct-26	17-Dec-26	$000	$000	$000	0.00
ML TX02-004-PR-12070	Staging time	5.00	100%	0%	20-Aug-26	25-Aug-26	13-Dec-26	17-Dec-26	$000	$000	$000	0.00
ML TX02-004-PR-11680	Material Delivery for Pressure Units	2000	100%	0%	22-Jul-26	13-Aug-26	14-Nov-26	06-Dec-26	$000	$000	$000	0.00
ML TX02-004-PR-12030	Material Fabrication for Pressure Units	1500	100%	0%	05-Jul-26	21-Jul-26	27-Oct-26	12-Nov-26	$000	$000	$000	0.00
AIR LOCK DOORS		4000	0%	0%	05-Jul-26	19-Aug-26	27-Oct-26	12-Dec-26	$000	$000	$000	0.00
ML TX02-004-PR-12080	Staging time	5.00	100%	0%	15-Aug-26	19-Aug-26	07-Dec-26	12-Dec-26	$000	$000	$000	0.00
ML TX02-004-PR-11700	Material Delivery for Lock Doors	2000	100%	0%	22-Jul-26	13-Aug-26	14-Nov-26	06-Dec-26	$000	$000	$000	0.00
ML TX02-004-PR-12040	Material Fabrication for Lock Doors	1500	100%	0%	05-Jul-26	21-Jul-26	27-Oct-26	12-Nov-26	$000	$000	$000	0.00
CONSTRUCTON PHASE		13.00	3793%	181%	12-Sep-26	25-Jan-27	16-Aug-26*	01-Apr-27	$3288,900.98	$ 156,902.66	$8669,997.04	-7600
SITE WORKS		13.00	3669%	1936%	12-Sep-26	25-Jan-27	16-Aug-26*	01-Apr-27	$2975,047.50	$ 156,902.66	$8108,244.72	-7600
LANDSCAPE WORKS		13.00	3794%	1952%	12-Sep-26	25-Jan-27	16-Aug-26*	01-Apr-27	$2975,047.50	$ 156,902.66	$8039,995.70	-7600
PLAYGROUND AREA		108.00	5243%	1949%	21-Sep-26	05-Jan-27	12-Oct-26A	25-Feb-27	$ 427,797.50	$159,046.88	$815,993.75	-2600
FOOTBALL PLAYGROUND		69.00	625%	2813%	21-Sep-26	21-Nov-26	12-Oct-26A	10-Feb-27	$ 148,812.50	$64715.63	$220,100.00	-5300
MLTX02-004-CN-13540	Install Sport Equipments- Goal / Nets - (FootballPlayground)	10.00	0%	0%	10-Nov-26	21-Nov-26	31-Jan-27	10-Feb-27	$000	$000	$71906.25	0.00
MLTX02-004-CN-13550	Suface Making and Painting(Football Playground)	10.00	0%	0%	27-Oct-26	07-Nov-26	10-Dec-26	21-Dec-26	$000	$000	$14381.25	0.00
MLTX02-004-CN-13530	Finishingand SurfaceFinishWorks(Football Playground)	15.00	100%	45%	21-Sep-26	08-Oct-26	12-Oct-26A	12-Nov-26	$ 148,812.50	$64715.63	$148,812.50	-13.00
PADEL PLAY GROUND		62.00	5556%	25%	21-Sep-26	21-Nov-26	20-Oct-26A	10-Feb-27	$58,625.00	$24131.25	$96525.00	-46.00
MLTX02-004-CN-13590	Install Sport Equipments- Goal / Nets - (Padel Playground)	10.00	0%	0%	10-Nov-26	21-Nov-26	31-Jan-27	10-Feb-27	$000	$000	$32175.00	0.00
MLTX02-004-CN-13600	Suface Making and Painting(Padel Playground)	10.00	0%	0%	10-Nov-26	21-Nov-26	31-Jan-27	10-Feb-27	$000	$000	$10725.00	0.00
MLTX02-004-CN-13580	Finishingand SurfaceFinishWorks(Padel Playground)	15.00	100%	45%	21-Sep-26	08-Oct-26	20-Oct-26A	05-Dec-26	$58,625.00	$24131.25	$53625.00	-25.00
BASKETBALL PLAY GROUND		59.00	625%	2813%	10-Oct-26	05-Dec-26	20-Oct-26A	25-Feb-27	$ 166,000.00	$70200.00	$246,600.00	-61.00
MLTX02-004-CN-13640	Install Sport Equipments- Goal / Nets - (Basketball Playground)	10.00	0%	0%	22-Nov-26	02-Dec-26	11-Feb-27	23-Feb-27	$000	$000	$78000.00	0.00
MLTX02-004-CN-13650	Suface Making and Painting(BasketballPlaygound)	12.00	0%	0%	22-Nov-26	05-Dec-26	11-Feb-27	25-Feb-27	$000	$000	$15600.00	0.00
MLTX02-004-CN-13630	Finishingand SurfaceFinishWorks(BasketballPlayground)	15.00	100%	45%	10-Oct-26	26-Oct-26	20-Oct-26A	05-Dec-26	$ 166,000.00	$70200.00	$156,000.00	-25.00
PADEL FENCE		26.00	0%	0%	13-Dec-26	05-Jan-27	27-Oct-26	25-Nov-26	$000	$000	$53868.75	-5.00
MLTX02-004-CN-13680	Tempered Glass Fence Installation and Fixation	10.00	0%	0%	13-Dec-26	23-Dec-26	27-Oct-26	07-Nov-26	$000	$000	$33150.00	0.00
MLTX02-004-CN-13690	Chain Link Fence Installation andFixation	10.00	0%	0%	13-Dec-26	23-Dec-26	14-Nov-26	24-Nov-26	$000	$000	$16575.00	0.00
MLTX02-004-CN-13700	Install ofFenceGates	11.00	0%	0%	24-Dec-26	05-Jan-27	14-Nov-26	25-Nov-26	$000	$000	$4143.75	0.00
CURBSTONE INTERLOCK		15.00	40%	0%	20-Oct-26	05-Nov-26	27-Oct-26	12-Nov-26	$74,340.00	$000	$185,900.00	0.00
MLTX02-004-CN-13390	Interlock Installation (Grey Stale) for LandScape (InludingFinishing Works)	15.00	40%	0%	20-Oct-26	05-Nov-26	27-Oct-26	12-Nov-26	$74,340.00	$000	$185,900.00	0.00
AIRDOME		110.00	5163%	1193%	12-Sep-26	04-Jan-27	24-Sep-26*	16-Mar-27	$2547,250.00	$588.65625	$4933,500.00	-47.00
CIVIL WORKS		39.00	100%	30%	12-Sep-26	05-Oct-26	24-Sep-26*	19-Dec-26	$1681,875.00	$504.56250	$1681,875.00	-5.400
MLTX02-004-CN-13740	Install ofMembraneCovering System (Air Dome)	12.00	100%	0%	21-Sep-26	05-Oct-26	06-Dec-26	19-Dec-26	$ 560.62500	$000	$560.62500	0.00
MLTX02-004-CN-13750	Thermal Insulation Works(Air Dome)	6.00	100%	0%	21-Sep-26	28-Sep-26	13-Dec-26	19-Dec-26	$ 560.62500	$000	$560.62500	0.00
MLTX02-004-CN-13730	Cable System Installation (AirDome)	8.00	100%	90%	12-Sep-26	20-Sep-26	24-Sep-26*	05-Dec-26	$ 560.62500	$504.56250	$560.62500	-5400
MECHANICAL WORKS		36.00	5885%	0%	29-Sep-26	09-Nov-26	20-Dec-26	30-Jan-27	$ 659.81250	$000	$1121.25000	0.00
MLTX02-004-CN-13780	AirDuctsand Gills Installation (Air Dome)	13.00	100%	0%	29-Sep-26	13-Oct-26	20-Dec-26	03-Jan-27	$ 280.31250	$000	$280.31250	0.00
MLTX02-004-CN-13790	AirUnits Installation (Air Dome)	13.00	8462%	0%	14-Oct-26	28-Oct-26	04-Jan-27	18-Jan-27	$ 359.50000	$000	$449.50000	0.00
MLTX02-004-CN-13800	Exhaust Fans and Ducts Installatin (AirDome)	10.00	0%	0%	29-Oct-26	09-Nov-26	19-Jan-27	30-Jan-27	$000	$000	$337.43750	0.00
ELECTRICAL WORKS		59.00	1222%	5%	14-Oct-26	04-Jan-27	15-Oct-26A	04-Mar-27	$ 215.56250	$84093.75	$1681,875.00	-49.00
MLTX02-004-CN-13820	Distribution Board andElectrical Works (Air Dome)	15.00	0%	0%	07-Nov-26	23-Nov-26	04-Jan-27	20-Jan-27	$000	$000	$281.31250	0.00
MLTX02-004-CN-13830	External Electrical Comection Works (Air Dome)	15.00	0%	0%	24-Nov-26	10-Dec-26	21-Jan-27	07-Feb-27	$000	$000	$281.31250	0.00
MLTX02-004-CN-13840	Emegency Generator Installation (Air Dome)	11.00	0%	0%	12-Dec-26	23-Dec-26	08-Feb-27	20-Feb-27	$000	$000	$550.62500	0.00
MLTX02-004-CN-13850	Control System Installation (Air Dome)	10.00	0%	0%	24-Dec-26	04-Jan-27	21-Feb-27	04-Mar-27	$000	$000	$281.31250	0.00
MLTX02-004-CN-13810	Light Fixture Works (AirDome)	15.00	7333%	30%	14-Oct-26	31-Oct-26	15-Oct-26A	03-Jan-27	$ 215.56250	$84093.75	$281.31250	-54.00
FINISHE SWORKS		43.00	0%	0%	24-Nov-26	26-Dec-26	21-Jan-27	16-Mar-27	$000	$000	$449.50000	-15.00
MLTX02-004-CN-13760	Doors Installation IncludingEmergency, Entrance doors (AirDome)	15.00	0%	0%	24-Nov-26	10-Dec-26	21-Jan-27	07-Feb-27	$000	$000	$224.25000	0.00
MLTX02-004-CN-13770	Logo andSigns Installation (Air Dome)	13.00	0%	0%	12-Dec-26	26-Dec-26	27-Feb-27	16-Mar-27	$000	$000	$224.25000	0.00
IRRIGATION NETWORK		60.00	0%	4014%	09-Nov-26	21-Nov-26	15-Sep-26*	07-Dec-26	$000	$37180.00	$92625.00	-60.00
ML TX02-004-CN-14450	Installingof Bubblersand Sprayes	30.00	0%	0%	18-Nov-26	21-Nov-26	05-Dec-26	07-Dec-26	$000	$000	$46150.00	0.00
ML TX02-004-CN-14640	Installingof Valves and fittings for Irrigation Network	30.00	0%	80%	09-Nov-26	11-Nov-26	15-Sep-26*	28-Nov-26	$000	$37180.00	$46475.00	-60.00
NATURAL GROUND		50.00	0%	0%	12-Nov-26	17-Nov-26	29-Nov-26	03-Dec-26	$000	$000	$117,000.00	0.00
ML TX02-004-CN-13420	Compacted Natural Ground Soil Installation Works for Lantscape	50.00	0%	0%	12-Nov-26	17-Nov-26	29-Nov-26	03-Dec-26	$000	$000	$117,000.00	0.00
PLANTING		120.00	0%	8.32%	22-Nov-26	12-Dec-26	12-Oct-26A	20-Dec-26	$000	$73573.50	$884,633.75	-42.00
ML TX02-004-CN-13480	Placementof Sweet/Agricultual Soil(Including levelling and Grading)	50.00	0%	0%	22-Nov-26	26-Nov-26	08-Dec-26	13-Dec-26	$000	$000	$321,945.00	0.00
ML TX02-004-CN-13500	Placementand Fixationof Trees	60.00	0%	0%	28-Nov-26	03-Dec-26	14-Dec-26	20-Dec-26	$000	$000	$387,515.75	0.00
ML TX02-004-CN-13490	Placementof Lawn Ground Cover (Rolling and Compaction)	70.00	0%	42%	05-Dec-26	12-Dec-26	12-Oct-26A	03-Nov-26	$000	$73573.50	$175,175.00	-13.00
WALKING/BIKE PATHS		80.00	0%	50%	13-Dec-26	21-Dec-26	16-Aug-26*	07-Nov-26	$000	$276.41250	$552,825.01	-63.00
ML TX02-004-CN-13460	Bike PathPreparationand Installation Works	80.00	0%	50%	13-Dec-26	21-Dec-26	16-Aug-26*	07-Nov-26	$000	$142.04532	$284,090.63	-63.00
ML TX02-004-CN-13440	Walking Path Preparation andInstallationWorks	80.00	0%	50%	13-Dec-26	21-Dec-26	16-Aug-26*	04-Nov-26	$000	$134.36719	$268,734.38	-61.00
GENERAL FURNITURE		122.00	0%	6757%	22-Dec-26	25-Jan-27	04-Oct-26A	01-Apr-27	$000	$434.73353	$648,418.20	-121.00
ML TX02-004-CN-13400	Stamped Concrete Works for LandScape (InludingFinishing Works)	70.00	0%	0%	22-Dec-26	29-Dec-26	20-Mar-27	27-Mar-27	$000	$000	$28080.00	0.00
ML TX02-004-CN-13470	Traffic Signs Posts and Poles Installation	50.00	0%	0%	13-Jan-27	18-Jan-27	28-Mar-27	01-Apr-27	$000	$000	$9750.00	0.00
ML TX02-004-CN-13870	Fixation and Installaiton of Steel Rame for Benches	10.00	0%	0%	22-Dec-26	02-Jan-27	08-Nov-26	18-Nov-26	$000	$000	$17276.63	0.00
ML TX02-004-CN-13880	Fixation and Installaiton of Benches	90.00	0%	0%	03-Jan-27	12-Jan-27	19-Nov-26	29-Nov-26	$000	$000	$40310.63	0.00
ML TX02-004-CN-13890	Fixation and Installaiton of Precast Concrete Stats (Rectangular)	90.00	0%	0%	03-Jan-27	12-Jan-27	19-Nov-26	29-Nov-26	$000	$000	$43680.00	0.00
ML TX02-004-CN-13900	Fixation and Installaiton of Precast Concrete Stats (Circular)	90.00	0%	0%	03-Jan-27	12-Jan-27	19-Nov-26	29-Nov-26	$000	$000	$17160.00	0.00
ML TX02-004-CN-13910	Fixation and Installaiton of Precast Concrete Trash Bins	110.00	0%	0%	13-Jan-27	25-Jan-27	21-Dec-26	02-Jan-27	$000	$000	$14625.00	0.00
ML TX02-004-CN-14350	Installingof SiteLightPoles	120.00	0%	92%	30-Dec-26	12-Jan-27	04-Oct-26A	27-Mar-27	$000	$434.73353	$472.53645	-134.00
PARKING		80.00	0%	0%	04-Jan-27	12-Jan-27	27-Oct-26	04-Nov-26	$000	$000	$68249.02	0.00
MLTX02-004-CN-13370	Interlock Installation (8 Cm) for Parking Area (InludingFinishing Works)	80.00	0%	0%	04-Jan-27	12-Jan-27	27-Oct-26	04-Nov-26	$000	$000	$68249.02	0.00
TOILET/SERVICE BUILDING		350.00	5587%	0%	15-Sep-26	16-Nov-26	27-Oct-26	06-Dec-26	$ 310.85348	$000	$561,752.32	180.0
MECHANICAL WORK		280.00	8257%	0%	17-Sep-26	08-Nov-26	27-Oct-26	28-Nov-26	$ 227.29688	$000	$275,268.88	160.0
HVAC SYSTEM		60.00	0%	0%	02-Nov-26	08-Nov-26	22-Nov-26	28-Nov-26	$000	$000	$14625.00	0.00
ML TX02-004-CN-14160	Install and Finish HVAC and Ventilation Works Including Split Air Units	60.00	0%	0%	02-Nov-26	08-Nov-26	22-Nov-26	28-Nov-26	$000	$000	$14625.00	0.00
WATER SUPPLY SYSTEM		100.00	100%	0%	21-Sep-26	13-Oct-26	27-Oct-26	07-Nov-26	$ 204.75000	$000	$204,750.00	9.00
ML TX02-004-CN-14120	Installingof Booster Pump Units Inludingfittings and accessories	50.00	100%	0%	08-Oct-26	13-Oct-26	02-Nov-26	07-Nov-26	$91,000.00	$000	$91000.00	0.00
ML TX02-004-CN-14210	Installingof GRP Tanks	50.00	100%	0%	03-Oct-26	07-Oct-26	27-Oct-26	01-Nov-26	$ 104,000.00	$000	$104,000.00	0.00
ML TX02-004-CN-14600	Installingof Valves and Fittings	40.00	100%	0%	21-Sep-26	26-Sep-26	27-Oct-26	31-Oct-26	$9750.00	$000	$9750.00	0.00



Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work


TASK filter: Remaining work

© Oracle Corporation

MLTX-02-004 - Playground Initiative for Western Region (Asir-Jazan -Jeddah)

Remaining work
D.D 26-10-2026

Activity ID	Activity Name	Original Duration	Schedule %	Performance % Complete	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Variance - BL Project
	SEWER/DRAINAGE SYSTEM	2000	418%	0%	17-Sep-26	29-Oct-26	27-Oct-26	18-Nov-26	$2,546.88	$000	$53941.88	1600
	ML TX0 2-004-CN-14230 Installing of Plumping Fixtures and Accessories	4 00	100%	0%	29-Sep-26	03-Oct-26	01-Nov-26	04-Nov-26	$10,359.38	$000	$10359.38	0.00
	ML TX0 2-004-CN-14680 Installing Inspection Chamber for Sewage Network	5 00	100%	0%	17-Sep-26	22-Sep-26	27-Oct-26	01-Nov-26	$12,187.50	$000	$12187.50	0.00
	ML TX0 2-004-CN-14700 Installing of Toilet Fixtures and Accessories Such as Closets and Basins	3 00	0%	0%	27-Oct-26	29-Oct-26	16-Nov-26	18-Nov-26	$000	$000	$31395.00	0.00
	FIRE PROJECTION	4 00	0%	0%	04-Nov-26	08-Nov-26	24-Nov-26	28-Nov-26	$000	$000	$1950.00	0.00
	ML TX0 2-004-CN-14240 Installing of Fire Fighting Extinguisher and accessories (PIE-1, PIE-2)	4 00	0%	0%	04-Nov-26	08-Nov-26	24-Nov-26	28-Nov-26	$000	$000	$1950.00	0.00
	ELECTRICAL WORKS	1300	0%	0%	02-Nov-26	16-Nov-26	22-Nov-26	06-Dec-26	$000	$000	$105,322.39	0.00
	FIXTURE WORKS	1300	0%	0%	02-Nov-26	16-Nov-26	22-Nov-26	06-Dec-26	$000	$000	$105,322.39	0.00
	ML TX0 2-004-CN-14250 Installing of Fire automation and Fire Alarm System	7 00	0%	0%	09-Nov-26	16-Nov-26	29-Nov-26	06-Dec-26	$000	$000	$34320.00	0.00
	ML TX0 2-004-CN-14320 Installing and Finalize Works of Lighting Works including Light Fixtures	4 00	0%	0%	04-Nov-26	08-Nov-26	24-Nov-26	28-Nov-26	$000	$000	$16050.00	0.00
	ML TX0 2-004-CN-14340 Installing Data and Telecommunication System with all Accessories	4 00	0%	0%	04-Nov-26	08-Nov-26	24-Nov-26	28-Nov-26	$000	$000	$18427.50	0.00
	ML TX0 2-004-CN-14380 Installing and Finalize Works of Security and Access Control System	6 00	0%	0%	02-Nov-26	08-Nov-26	22-Nov-26	28-Nov-26	$000	$000	$22899.88	0.00
	ML TX0 2-004-CN-14400 Installing and Finalize Works of Lightning Protection System	6 00	0%	0%	02-Nov-26	08-Nov-26	22-Nov-26	28-Nov-26	$000	$000	$14625.00	0.00
	DOORS/WINDOWS	2600	40%	0%	15-Sep-26	05-Nov-26	27-Oct-26	25-Nov-26	$28,400.00	$000	$58500.00	1800
	MLTX02-004-CN-14470 Finalize Glazed Curtain Wall Works	4 00	0%	0%	02-Nov-26	05-Nov-26	22-Nov-26	25-Nov-26	$000	$000	$35100.00	0.00
	MLTX02-004-CN-14550 Preliminary Works for Windows/Curtain Wall	2 00	100%	0%	15-Sep-26	16-Sep-26	27-Oct-26	28-Oct-26	$23,400.00	$000	$23400.00	0.00
	FINISHING WORKS	2400	7684%	0%	30-Sep-26	03-Nov-26	27-Oct-26	23-Nov-26	$48,531.88	$000	$63156.88	6.00
	FLOOR FINISHES	4 00	100%	0%	05-Oct-26	08-Oct-26	27-Oct-26	31-Oct-26	$2925.00	$000	$2925.00	0.00
	ML TX0 2-004-CN-14480 Granite Tiles Floor Finish Works	4 00	100%	0%	05-Oct-26	08-Oct-26	27-Oct-26	31-Oct-26	$2925.00	$000	$2925.00	0.00
	WALL FINISHES	2400	729%	0%	10-Oct-26	03-Nov-26	27-Oct-26	23-Nov-26	$36,381.00	$000	$53976.00	-2.00
	ML TX0 2-004-CN-14450 Phenolic Partitions for Toilets	5 00	100%	0%	21-Oct-26	26-Oct-26	10-Nov-26	15-Nov-26	$31,200.00	$000	$31200.00	0.00
	ML TX0 2-004-CN-14570 Glass Partitions including all accessories and doors	5 00	0%	0%	27-Oct-26	01-Nov-26	16-Nov-26	21-Nov-26	$000	$000	$12285.00	0.00
	ML TX0 2-004-CN-14580 Granite Capping for Papet	2 00	100%	0%	10-Oct-26	11-Oct-26	27-Oct-26	28-Oct-26	$8151.00	$000	$8151.00	0.00
	ML TX0 2-004-CN-14670 Painting Finish Works for Internal Walls	2 00	0%	0%	02-Nov-26	03-Nov-26	22-Nov-26	23-Nov-26	$000	$000	$2340.00	0.00
	CEILING FINISHES	1300	100%	0%	30-Sep-26	24-Oct-26	27-Oct-26	10-Nov-26	$6255.60	$000	$6255.60	8.00
	ML TX0 2-004-CN-14710 Painting Finish Works for Ceiling	3 00	100%	0%	21-Oct-26	24-Oct-26	08-Nov-26	10-Nov-26	$1638.00	$000	$1638.00	0.00
	ML TX0 2-004-CN-14730 Preliminary Works & Ceiling Painting Works	1000	100%	0%	30-Sep-26	11-Oct-26	27-Oct-26	07-Nov-26	$4617.60	$000	$4617.60	0.00
	SPECIALTIES WORK	2600	75%	0%	04-Oct-26	15-Nov-26	05-Nov-26	05-Dec-26	$14,625.00	$000	$58500.00	1100
	MLTX02-004-CN-14130 Sanitary Fixtures and Accessories Works	4 00	100%	0%	04-Oct-26	07-Oct-26	05-Nov-26	09-Nov-26	$14,625.00	$000	$14625.00	0.00
	MLTX02-004-CN-14140 Installation of MODON Logo on the entrance	1000	0%	0%	04-Nov-26	15-Nov-26	24-Nov-26	05-Dec-26	$000	$000	$19506.45	0.00
	MLTX02-004-CN-14590 Installation of Phenolic Locker	2 00	0%	0%	27-Oct-26	28-Oct-26	16-Nov-26	17-Nov-26	$000	$000	$24375.00	0.00
	TESTING & COMMISSIONING	9500	0%	0%	01-Dec-26	18-Jan-27	08-Dec-26	01-Apr-27	$000	$000	$000	-5300
	MLTX02-004-TC-11920 Testing and Commissioning for MEP Works for Playground Area	8 00	0%	0%	05-Jan-27	13-Jan-27	17-Mar-27	25-Mar-27	$000	$000	$000	0.00
	MLTX02-004-TC-11930 Testing and Commissioning for MEP Works for Toilet/Service Building	1500	0%	0%	01-Dec-26	17-Dec-26	08-Dec-26	24-Dec-26	$000	$000	$000	0.00
	MLTX02-004-TC-11940 Testing and Commissioning for MEP Works for Landscape Works	4 00	0%	0%	14-Jan-27	18-Jan-27	29-Mar-27	01-Apr-27	$000	$000	$000	0.00
	ASIR	145.00	1258%	1359%	05-Jul-26	24-Jan-27	11-Aug-26	18-Apr-27	$ 99,182.79	$ 100,420.17	$7387,515.96	-3600
	ENGINEERING	3600	0%	0%	05-Jul-26	02-Sep-26	27-Oct-26	07-Dec-26	$000	$000	$000	1600
	METHOD STATEMENTS	1600	0%	0%	05-Jul-26	22-Jul-26	27-Oct-26	14-Nov-26	$000	$000	$000	0.00
	METHOD STATEMENT SUBMITTAL	600	0%	0%	05-Jul-26	11-Jul-26	27-Oct-26	02-Nov-26	$000	$000	$000	0.00
	ARCHITECTURE WORKS	600	0%	0%	05-Jul-26	11-Jul-26	27-Oct-26	02-Nov-26	$000	$000	$000	0.00
	ML TX0 2-004-EN-4140 Preparation & Submission of Method Statement for Fence Works	600	100%	0%	05-Jul-26	11-Jul-26	27-Oct-26	02-Nov-26	$000	$000	$000	0.00
	METHOD STATEMENT APPROVAL	1000	0%	0%	12-Jul-26	22-Jul-26	03-Nov-26	14-Nov-26	$000	$000	$000	0.00
	ARCHITECTURE WORKS	1000	0%	0%	12-Jul-26	22-Jul-26	03-Nov-26	14-Nov-26	$000	$000	$000	0.00
	ML TX0 2-004-EN-4160 Approval of Method Statement for Fence Works	1000	100%	0%	12-Jul-26	22-Jul-26	03-Nov-26	14-Nov-26	$000	$000	$000	0.00
	PREQUALIFICATION & MATERIAL	3600	0%	0%	05-Jul-26	02-Sep-26	27-Oct-26	07-Dec-26	$000	$000	$000	1600
	MATERIAL SUBMITTAL & APPROVAL	3600	0%	0%	05-Jul-26	02-Sep-26	27-Oct-26	07-Dec-26	$000	$000	$000	1600
	PLAYGROUND WORKS	3600	0%	0%	05-Jul-26	02-Sep-26	27-Oct-26	07-Dec-26	$000	$000	$000	1600
	PVC MEMBRANE	800	0%	0%	05-Jul-26	13-Jul-26	27-Oct-26	04-Nov-26	$000	$000	$000	0.00
	ML TX0 2-004-EN-4880 Material Approval for PVC Membrane	800	100%	0%	05-Jul-26	13-Jul-26	27-Oct-26	04-Nov-26	$000	$000	$000	0.00
	STEEL TENSION CABLES	900	0%	0%	14-Jul-26	23-Jul-26	05-Nov-26	15-Nov-26	$000	$000	$000	0.00
	ML TX0 2-004-EN-4910 Material Approval for Steel Tension Cables	900	100%	0%	14-Jul-26	23-Jul-26	05-Nov-26	15-Nov-26	$000	$000	$000	0.00
	EMERGENCY DOORS	900	0%	0%	25-Jul-26	03-Aug-26	16-Nov-26	25-Nov-26	$000	$000	$000	0.00
	ML TX0 2-004-EN-4940 Material Approval for Emergency Doors	900	100%	0%	25-Jul-26	03-Aug-26	16-Nov-26	25-Nov-26	$000	$000	$000	0.00
	AIR LOCK DOORS	800	0%	0%	16-Aug-26	24-Aug-26	19-Nov-26	28-Nov-26	$000	$000	$000	0.00
	ML TX0 2-004-EN-7000 Material Approval for Lock Doors	800	100%	0%	16-Aug-26	24-Aug-26	19-Nov-26	28-Nov-26	$000	$000	$000	0.00
	PADEL WIREMESH/STEEL SETS	800	0%	0%	25-Aug-26	02-Sep-26	29-Nov-26	07-Dec-26	$000	$000	$000	0.00
	ML TX0 2-004-EN-7120 Material Approval for WireMesh/Steel Sets	800	100%	0%	25-Aug-26	02-Sep-26	29-Nov-26	07-Dec-26	$000	$000	$000	0.00
	PROCUREMENT	8900	0%	0%	05-Jul-26	17-Oct-26	27-Oct-26	07-Feb-27	$000	$000	$000	0.00
	SHORT LEAD ITEM	7800	0%	0%	05-Jul-26	12-Oct-26	27-Oct-26	25-Jan-27	$000	$000	$000	7.00
	TOILETS/SERVICE WORKS	2000	0%	0%	05-Jul-26	27-Jul-26	27-Oct-26	18-Nov-26	$000	$000	$000	0.00
	PACKAGEAC UNITS	1500	0%	0%	05-Jul-26	21-Jul-26	27-Oct-26	12-Nov-26	$000	$000	$000	0.00
	ML TX0 2-004-PR-8830 Material Delivery for Package AC Units	1500	100%	0%	05-Jul-26	21-Jul-26	27-Oct-26	12-Nov-26	$000	$000	$000	0.00
	LIGHTING FIXTURES	1000	0%	0%	05-Jul-26	15-Jul-26	27-Oct-26	07-Nov-26	$000	$000	$000	0.00
	ML TX0 2-004-PR-8850 Material Delivery for Lighting Fixtures	1000	100%	0%	05-Jul-26	15-Jul-26	27-Oct-26	07-Nov-26	$000	$000	$000	0.00
	SWITCHES/SOCKETS	700	0%	0%	05-Jul-26	12-Jul-26	27-Oct-26	03-Nov-26	$000	$000	$000	0.00
	ML TX0 2-004-PR-8530 Material Delivery for Switches/Sockets	700	100%	0%	05-Jul-26	12-Jul-26	27-Oct-26	03-Nov-26	$000	$000	$000	0.00
	DISTRIBUTION PANELS	1500	0%	0%	11-Jul-26	27-Jul-26	27-Oct-26	12-Nov-26	$000	$000	$000	0.00
	ML TX0 2-004-PR-8510 Material Delivery for Distribution Panels	1500	100%	0%	11-Jul-26	27-Jul-26	27-Oct-26	12-Nov-26	$000	$000	$000	0.00
	FURNITURES	2000	0%	0%	05-Jul-26	27-Jul-26	27-Oct-26	18-Nov-26	$000	$000	$000	0.00
	ML TX0 2-004-PR-8170 Material Delivery for Furnitures	2000	100%	0%	05-Jul-26	27-Jul-26	27-Oct-26	18-Nov-26	$000	$000	$000	0.00
	PLAYGROUND WORKS	3000	0%	0%	05-Jul-26	01-Sep-26	27-Oct-26	30-Nov-26	$000	$000	$000	2100
	PVC MEMBRANE	400	0%	0%	05-Jul-26	08-Jul-26	27-Oct-26	31-Oct-26	$000	$000	$000	0.00
	ML TX0 2-004-PR-8650 Material Delivery for PVC Membrane	400	100%	0%	05-Jul-26	08-Jul-26	27-Oct-26	31-Oct-26	$000	$000	$000	0.00
	ARTIFICIAL TURF	1200	0%	0%	09-Jul-26	22-Jul-26	01-Nov-26	14-Nov-26	$000	$000	$000	0.00
	ML TX0 2-004-PR-8850 Material Delivery for Artificial TURF	1200	100%	0%	09-Jul-26	22-Jul-26	01-Nov-26	14-Nov-26	$000	$000	$000	0.00
	PADEL GLASS	1800	0%	0%	05-Jul-26	25-Jul-26	27-Oct-26	16-Nov-26	$000	$000	$000	0.00
	ML TX0 2-004-PR-8930 Material Delivery for Padel Glass	1800	100%	0%	05-Jul-26	25-Jul-26	27-Oct-26	16-Nov-26	$000	$000	$000	0.00
	PADEL WIREMESH/STEEL SETS	1600	0%	0%	05-Jul-26	22-Jul-26	27-Oct-26	14-Nov-26	$000	$000	$000	0.00
	ML TX0 2-004-PR-8970 Material Delivery for WireMesh/Steel Sets	1600	100%	0%	05-Jul-26	22-Jul-26	27-Oct-26	14-Nov-26	$000	$000	$000	0.00
	INTERLOCKING PAVING	700	0%	0%	05-Jul-26	12-Jul-26	27-Oct-26	03-Nov-26	$000	$000	$000	0.00
	ML TX0 2-004-PR-9070 Material Delivery for Interlocking Block Pavers	700	100%	0%	05-Jul-26	12-Jul-26	27-Oct-26	03-Nov-26	$000	$000	$000	0.00
	MARKING PAINT	700	0%	0%	11-Jul-26	18-Jul-26	27-Oct-26	03-Nov-26	$000	$000	$000	0.00
	ML TX0 2-004-PR-9110 Material Delivery for Marking Paint	700	100%	0%	11-Jul-26	18-Jul-26	27-Oct-26	03-Nov-26	$000	$000	$000	0.00
	PACKAGEAC UNITS	1500	0%	0%	05-Jul-26	21-Jul-26	27-Oct-26	12-Nov-26	$000	$000	$000	0.00
	ML TX0 2-004-PR-9150 Material Delivery for Package AC Units	1500	100%	0%	05-Jul-26	21-Jul-26	27-Oct-26	12-Nov-26	$000	$000	$000	0.00

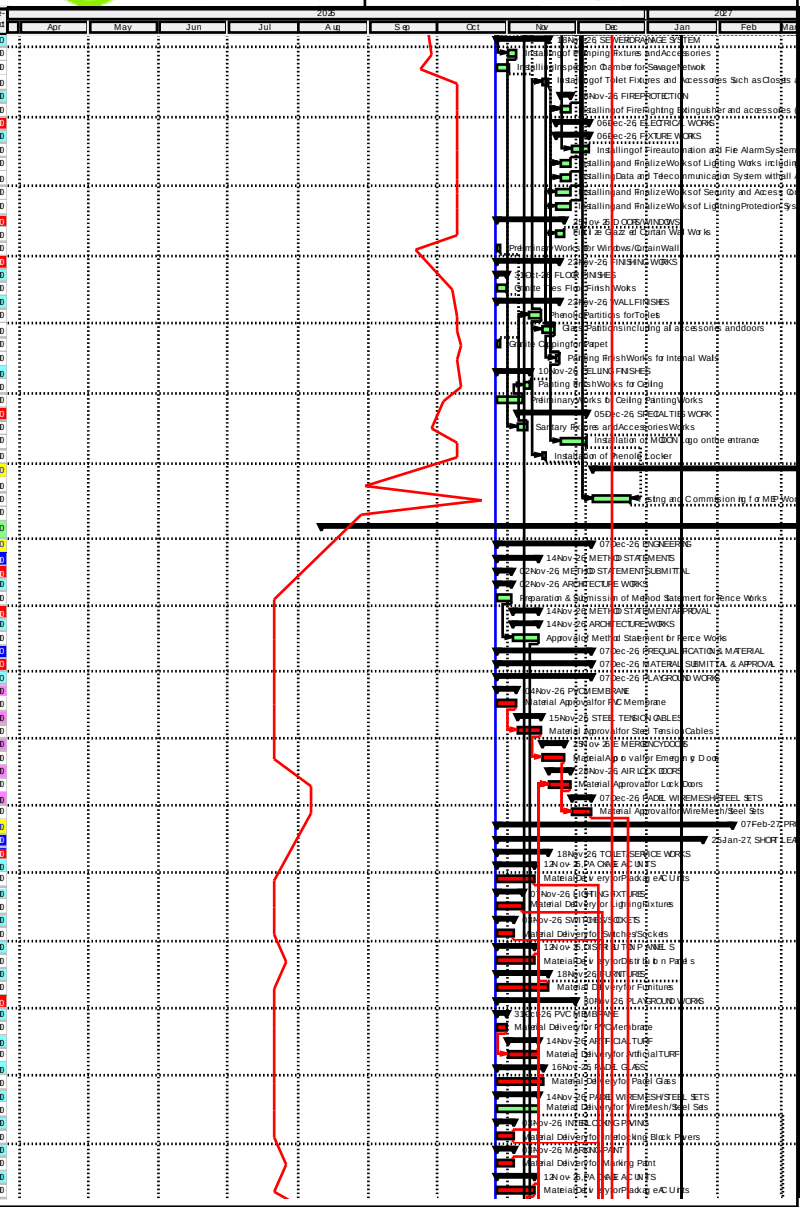

Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work


TASK filter: Remaining work

© Oracle Corporation

MLTX-02-004 - Playground Initiative for Western Region (Asir-Jazan -Jeddah)

Remaining work
D.D 26-10-2026

Activity ID	Activity Name	Original Duration	Schedule %	Performance % Complete	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Variance - BL Project
	DISTRIBUTION BOARDS	1500	0%	0%	29Jul-26	15Aug-26	27Oct-26	12Nov-26	$000	$000	$000	0.00
	ML TX0 2-004-PR-9810 Material Delivery for Distribution Boards	1500	100%	0%	29Jul-26	15Aug-26	27Oct-26	12Nov-26	$000	$000	$000	0.00
	POWER CABLES	1000	0%	0%	04Aug-26	15Aug-26	27Oct-26	07Nov-26	$000	$000	$000	0.00
	ML TX0 2-004-PR-9850 Material Delivery for Power Cables	1000	100%	0%	04Aug-26	15Aug-26	27Oct-26	07Nov-26	$000	$000	$000	0.00
	LIGHT FIXTURES	1600	0%	0%	05Jul-26	22Jul-26	27Oct-26	14Nov-26	$000	$000	$000	0.00
	ML TX0 2-004-PR-9890 Material Delivery for Light Fixtures	1600	100%	0%	05Jul-26	22Jul-26	27Oct-26	14Nov-26	$000	$000	$000	0.00
	CCTV MATERIALS	3000	0%	0%	12Jul-26	01Sep-26	27Oct-26	30Nov-26	$000	$000	$000	1500
	ML TX0 2-004-PR-9410 PO for CCTV	5 00	100%	0%	12Jul-26	16Jul-26	27Oct-26	01Nov-26	$000	$000	$000	0.00
	ML TX0 2-004-PR-9430 Material Delivery for CCTV	1500	100%	0%	16Aug-26	01Sep-26	14Nov-26	30Nov-26	$000	$000	$000	0.00
	POWER OUTLETS/SWITCHES	1500	0%	0%	29Jul-26	15Aug-26	27Oct-26	12Nov-26	$000	$000	$000	0.00
	ML TX0 2-004-PR-9470 Material Delivery for Power Outlets/Switches	1500	100%	0%	29Jul-26	15Aug-26	27Oct-26	12Nov-26	$000	$000	$000	0.00
	LANDSCAPE WORKS	7300	0%	0%	12Aug-26	12Oct-26	27Oct-26	25Jan-27	$000	$000	$000	-2600
	INTERLOCKING PAVING	1200	0%	0%	02Sep-26	15Sep-26	01Dec-26	14Dec-26	$000	$000	$000	0.00
	ML TX0 2-004-PR-9520 Material Delivery for Interlocking Block Pavers	1200	100%	0%	02Sep-26	15Sep-26	01Dec-26	14Dec-26	$000	$000	$000	0.00
	PAVEMENT MARKING	1000	0%	0%	12Aug-26	23Aug-26	27Oct-26	07Nov-26	$000	$000	$000	0.00
	ML TX0 2-004-PR-9600 Material Delivery for Pavement Markings	1000	100%	0%	12Aug-26	23Aug-26	27Oct-26	07Nov-26	$000	$000	$000	0.00
	TRAFFIC SIGNS	1400	0%	0%	16Sep-26	03Oct-26	09Jan-27	24Jan-27	$000	$000	$000	0.00
	ML TX0 2-004-PR-9620 PO for Traffic Signs	5 00	100%	0%	16Sep-26	21Sep-26	09Jan-27	13Jan-27	$000	$000	$000	0.00
	ML TX0 2-004-PR-9640 Material Delivery for Traffic Signs	9 00	100%	0%	22Sep-26	03Oct-26	14Jan-27	24Jan-27	$000	$000	$000	0.00
	AGRICULTURE SOIL	1200	0%	0%	29Sep-26	12Oct-26	27Oct-26	09Nov-26	$000	$000	$000	0.00
	ML TX0 2-004-PR-9720 Material Delivery for Agriculture Soil	1200	100%	0%	29Sep-26	12Oct-26	27Oct-26	09Nov-26	$000	$000	$000	0.00
	TRACK SURFACE	1500	0%	0%	05Sep-26	21Sep-26	28Dec-26	13Jan-27	$000	$000	$000	0.00
	ML TX0 2-004-PR-9740 PO for Track Surface	5 00	100%	0%	05Sep-26	09Sep-26	28Dec-26	02Jan-27	$000	$000	$000	0.00
	ML TX0 2-004-PR-9760 Material Delivery for Track Surface	1000	100%	0%	10Sep-26	21Sep-26	03Jan-27	13Jan-27	$000	$000	$000	0.00
	GRASS/TREES	2000	0%	0%	10Sep-26	04Oct-26	03Jan-27	25Jan-27	$000	$000	$000	0.00
	ML TX0 2-004-PR-9780 PO for Grass/Trees	5 00	100%	0%	10Sep-26	15Sep-26	03Jan-27	07Jan-27	$000	$000	$000	0.00
	ML TX0 2-004-PR-9800 Material Delivery for Grass/Trees	1500	100%	0%	16Sep-26	04Oct-26	09Jan-27	25Jan-27	$000	$000	$000	0.00
	LONG LEAD ITEM	8900	0%	0%	05Jul-26	17Oct-26	27Oct-26	07Feb-27	$000	$000	$000	0.00
	PLAYGROUND WORKS	8900	0%	0%	05Jul-26	17Oct-26	27Oct-26	07Feb-27	$000	$000	$000	0.00
	STEEL TENSION CABLES	8900	0%	0%	29Jul-26	17Oct-26	27Oct-26	07Feb-27	$000	$000	$000	-2100
	ML TX0 2-004-PR-9590 Material Delivery for Steel Tension Cables	2900	100%	0%	05Sep-26	08Oct-26	28Dec-26	30Jan-27	$000	$000	$000	0.00
	ML TX0 2-004-PR-9580 Material Fabrication for Steel Tension Cables	2000	100%	0%	29Jul-26	20Aug-26	27Oct-26	18Nov-26	$000	$000	$000	0.00
	ML TX0 2-004-PR-9990 Staging time	7 00	100%	0%	10Oct-26	17Oct-26	31Jan-27	07Feb-27	$000	$000	$000	0.00
	EMERGENCY DOORS	5300	0%	0%	05Jul-26	03Sep-26	27Oct-26	27Dec-26	$000	$000	$000	0.00
	ML TX0 2-004-PR-9730 Material Delivery for Emegency Doors	2500	100%	0%	28Jul-26	25Aug-26	19Nov-26	17Dec-26	$000	$000	$000	0.00
	ML TX0 2-004-PR-9720 Material Fabrication for Emergency Doors	2000	100%	0%	05Jul-26	27Jul-26	27Oct-26	18Nov-26	$000	$000	$000	0.00
	ML TX0 2-004-PR-9900 Staging time	8 00	100%	0%	26Aug-26	03Sep-26	19Dec-26	27Dec-26	$000	$000	$000	0.00
	PRESSURE UNITS	5300	0%	0%	05Jul-26	03Sep-26	27Oct-26	27Dec-26	$000	$000	$000	0.00
	ML TX0 2-004-PR-9770 Material Delivery for Pressure Units	2500	100%	0%	28Jul-26	25Aug-26	19Nov-26	17Dec-26	$000	$000	$000	0.00
	ML TX0 2-004-PR-9760 Material Fabrication for Pressure Units	2000	100%	0%	05Jul-26	27Jul-26	27Oct-26	18Nov-26	$000	$000	$000	0.00
	ML TX0 2-004-PR-9910 Staging time	8 00	100%	0%	26Aug-26	03Sep-26	19Dec-26	27Dec-26	$000	$000	$000	0.00
	AIRLOCK DOORS	5300	0%	0%	05Jul-26	03Sep-26	27Oct-26	27Dec-26	$000	$000	$000	0.00
	ML TX0 2-004-PR-9810 Material Delivery for Lock Doors	2500	100%	0%	28Jul-26	25Aug-26	19Nov-26	17Dec-26	$000	$000	$000	0.00
	ML TX0 2-004-PR-9800 Material Fabrication for Lock Doors	2000	100%	0%	05Jul-26	27Jul-26	27Oct-26	18Nov-26	$000	$000	$000	0.00
	ML TX0 2-004-PR-9920 Staging time	8 00	100%	0%	26Aug-26	03Sep-26	19Dec-26	27Dec-26	$000	$000	$000	0.00
	CONSTRUCTION PHASE	140.00	1258%	1359%	19Jul-26	24Jan-27	11Aug-26A	15Apr-27	$ 99,18279	$ 100 4 200 17	$7387.515.96	-4600
	SITE WORKS	140.00	3.88%	1505%	12Oct-26	24Jan-27	11Aug-26A	15Apr-27	$ 26.75688	$ 100 4 200 17	$6674.00 33	-138.00
	LANDSCAPE WORKS	140.00	3.88%	1505%	12Oct-26	24Jan-27	11Aug-26A	15Apr-27	$ 26.75688	$ 100 4 200 17	$6674.00 33	-138.00
	PLAYGROUND AREA	127.00	3066%	0%	12Oct-26	04Jan-27	27Oct-26	28Mar-27	$ 185.90000	$000	$665.36875	-5400
	FOOTBALL PLAYGROUND	193.00	0%	0%	29Oct-26	13Dec-26	27Oct-26	18Mar-27	$000	$000	$220.10000	-8000
	MLTX02-004-CN-10040 Finishing and Surface Finish Works (Football Playground)	3000	0%	0%	29Oct-26	02Dec-26	27Oct-26	30Nov-26	$000	$000	$145.81250	0.00
	MLTX02-004-CN-10050 Install Sport Equipments - Goal / Nets - (Football Playground)	9 00	0%	0%	03Dec-26	13Dec-26	06Mar-27	18Mar-27	$000	$000	$71906.25	0.00
	MLTX02-004-CN-10060 Surface Making and Painting (Football Playground)	8 00	0%	0%	03Dec-26	12Dec-26	06Mar-27	17Mar-27	$000	$000	$14381.25	0.00
	PADEL PLAY GROUND	1000	0%	0%	03Dec-26	14Dec-26	06Mar-27	20Mar-27	$000	$000	$42900.00	0.00
	MLTX02-004-CN-10110 Install Sport Equipments - Goal / Nets - (Padel Playground)	1000	0%	0%	03Dec-26	14Dec-26	06Mar-27	20Mar-27	$000	$000	$32175.00	0.00
	MLTX02-004-CN-10120 Surface Making and Painting (Padel Playground)	8 00	0%	0%	03Dec-26	12Dec-26	08Mar-27	20Mar-27	$000	$000	$10725.00	0.00
	BASKETBALL PLAYGROUND	1700	0%	0%	03Dec-26	20Dec-26	06Mar-27	28Mar-27	$000	$000	$93600.00	-2.00
	MLTX02-004-CN-10210 Install Sport Equipments - Goal / Nets - (Basketball Playground)	1500	0%	0%	03Dec-26	20Dec-26	06Mar-27	25Mar-27	$000	$000	$78000.00	0.00
	MLTX02-004-CN-10220 Surface Making and Painting (Basketball Playground)	7 00	0%	0%	13Dec-26	20Dec-26	21Mar-27	28Mar-27	$000	$000	$15600.00	0.00
	PADEL FENCE	4 00	0%	0%	31Dec-26	04Jan-27	15Nov-26	18Nov-26	$000	$000	$53868.75	0.00
	MLTX02-004-CN-10260 Tempered Glass Renc Installation and Fixation	2 00	0%	0%	31Dec-26	02Jan-27	15Nov-26	16Nov-26	$000	$000	$33150.00	0.00
	MLTX02-004-CN-10270 Chain Link Fence Installation and Fixation	2 00	0%	0%	03Jan-27	04Jan-27	17Nov-26	18Nov-26	$000	$000	$16575.00	0.00
	MLTX02-004-CN-10280 Install of Fence Gates	2 00	0%	0%	03Jan-27	04Jan-27	17Nov-26	18Nov-26	$000	$000	$4143.75	0.00
	CHRISTOPHE INTERLOCK	1000	100%	0%	12Oct-26	22Oct-26	15Dec-26	26Dec-26	$ 185.90000	$000	$185.90000	0.00
	MLTX02-004-CN-10140 Interlock Installation (Grey Stale) for Land Scape (Including Finishing Works)	1000	100%	0%	12Oct-26	22Oct-26	15Dec-26	26Dec-26	$ 185.90000	$000	$185.90000	0.00
	AIRDOME	4900	0%	7.41%	09Nov-26	31Dec-26	07Oct-26A	06Apr-27	$000	$325.16250	$4372.875.00	-105.00
	CIVIL WORKS	1700	0%	6%	09Nov-26	24Nov-26	21Oct-26A	24Feb-27	$000	$67275.00	$1121.250.00	-9400
	MLTX02-004-CN-10360 Install of Membrane Covering System (Air Dome)	1400	0%	0%	09Nov-26	24Nov-26	08Feb-27	24Feb-27	$000	$000	$550.62500	0.00
	MLTX02-004-CN-10370 Thermal Insulation Works (Air Dome)	1400	0%	12%	09Nov-26	24Nov-26	21Oct-26A	24Feb-27	$000	$67275.00	$550.62500	-9400
	MECHANICAL WORKS	1300	0%	0%	25Nov-26	09Dec-26	25Feb-27	15Mar-27	$000	$000	$1121.250.00	0.00
	MLTX02-004-CN-10410 Air Ducts and Grills Installation (Air Dome)	1000	0%	0%	25Nov-26	06Dec-26	25Feb-27	08Mar-27	$000	$000	$220.31250	0.00
	MLTX02-004-CN-10420 Air Units Installation (Air Dome)	1300	0%	0%	25Nov-26	09Dec-26	25Feb-27	15Mar-27	$000	$000	$440.50000	0.00
	MLTX02-004-CN-10430 Exhaust Fans and Ducts Installation (Air Dome)	7 00	0%	0%	25Nov-26	02Dec-26	25Feb-27	04Mar-27	$000	$000	$392.43750	0.00
	ELECTRICAL WORKS	3200	0%	1533%	10Dec-26	31Dec-26	07Oct-26A	06Apr-27	$000	$257.88750	$1681.875.00	-138.00
	MLTX02-004-CN-10460 Distribution Board and Electrical Works (Air Dome)	3 00	0%	0%	15Dec-26	17Dec-26	16Mar-27	18Mar-27	$000	$000	$220.31250	0.00
	MLTX02-004-CN-10470 External Electrical Comection Works (Air Dome)	4 00	0%	0%	19Dec-26	22Dec-26	20Mar-27	23Mar-27	$000	$000	$220.31250	0.00
	MLTX02-004-CN-10480 Emegency Generator Installation (Air Dome)	4 00	0%	0%	23Dec-26	27Dec-26	24Mar-27	28Mar-27	$000	$000	$550.62500	0.00
	MLTX02-004-CN-10490 Control System Installation (Air Dome)	4 00	0%	0%	28Dec-26	31Dec-26	03Apr-27	06Apr-27	$000	$000	$220.31250	0.00
	MLTX02-004-CN-10450 Light Fixture Works (AirDome)	4 00	0%	92%	10Dec-26	14Dec-26	07Oct-26A	15Mar-27	$000	$257.88750	$220.31250	-129.00
	FINISHE SWORKS	1500	0%	0%	10Dec-26	27Dec-26	16Mar-27	01Apr-27	$000	$000	$440.50000	0.00
	MLTX02-004-CN-10380 Doors Installation Including Emergency, Entrance doors (AirDome)	6 00	0%	0%	10Dec-26	16Dec-26	16Mar-27	22Mar-27	$000	$000	$220.25000	0.00
	MLTX02-004-CN-10390 Logo and Signs Installation (Air Dome)	9 00	0%	0%	17Dec-26	27Dec-26	23Mar-27	01Apr-27	$000	$000	$220.25000	0.00
	IRRIGATION NETWORK	4800	5018%	4014%	21Oct-26	04Nov-26	24Sep-26A	28Jan-27	$46,475.00	$37180.00	$92625.00	-9600
	ML TX0 2-004-CN-11450 Installing of Bubblers and Sprayes	3 00	0%	0%	02Nov-26	04Nov-26	26Jan-27	28Jan-27	$000	$000	$461.50.00	0.00
	ML TX0 2-004-CN-11450 Installing of Valves and fittings for Irrigation Network	4 00	100%	80%	21Oct-26	25Oct-26	24Sep-26A	21Dec-26	$46,475.00	$37180.00	$46475.00	-7200

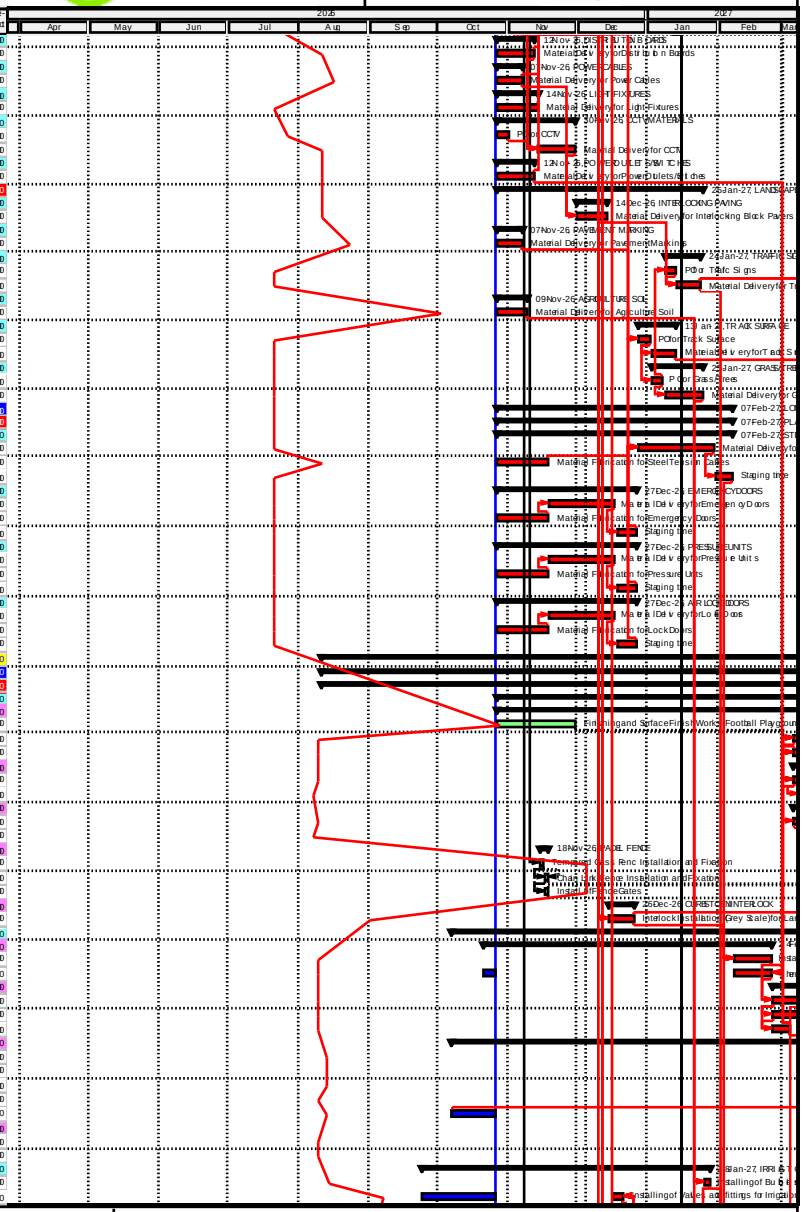

Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work


TASK filter: Remaining work

© Oracle Corporation

MLTX-02-004 - Playground Initiative for Western Region (Asir-Jazan -Jeddah)

Remaining work
D.D 26-10-2026

Activity ID	Activity Name	Original Duration	Schedule %	Performance % Complete	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Variance - BL Project
NATURAL GROUND		60	1667%	0%	26Oct-26	01Nov-26	27Dec-26	02Jan-27	$13,381.88	$000	$80291.25	0.00
ML TX0 2 004 CN 10550	CompactedNatural Ground Soil InstallationWorksfor Lantscape	60	1667%	0%	26Oct-26	01Nov-26	27Dec-26	02Jan-27	$13,381.88	$000	$80291.25	0.00
PLANTING		4600	0%	1154%	05Nov-26	13Dec-26	13Oct-26A	18Mar-27	$000	$68975.40	$597,83750	-9800
ML TX0 2 004 CN 10580	Placementof Lawn Ground Cover (Rolling and Compaction)	300	0%	0%	10Dec-26	13Dec-26	16Mar-27	18Mar-27	$000	$000	$175,17500	0.00
ML TX0 2 004 CN 10590	Placementand Fixationof Trees	300	0%	0%	07Dec-26	09Dec-26	09Mar-27	15Mar-27	$000	$000	$235.24250	0.00
ML TX0 2 004 CN 10570	Placementof Sweet/Agricultural Soil(Including Levelling andGrading)	300	0%	37%	05Nov-26	08Nov-26	13Oct-26A	28Jan-27	$000	$68975.40	$185.42000	-9000
WALKING/BIKE PATHS		1200	0%	50%	14Dec-26	27Dec-26	11Aug-26A	18Mar-27	$000	$138.20639	$276,41277	-1200
ML TX0 2 004 CN 10510	Bike PathPreparationand Installation Works	1200	0%	50%	14Dec-26	27Dec-26	11Aug-26A	18Mar-27	$000	$71022.68	$142,04536	-1200
ML TX0 2 004 CN 10520	Walking Path Preparation andInstallationWorks	1200	0%	50%	14Dec-26	27Dec-26	11Aug-26A	18Mar-27	$000	$67183.70	$136,36741	-1200
GENERAL FURNITURE		2700	0%	6712%	28Dec-26	24Jan-27	01Oct-26A	15Apr-27	$000	$431,67588	$647,59406	-1400
ML TX0 2 004 CN 10610	Stamped ConcreteWorksfor LandScape (IndudingFinishing Works)	900	0%	0%	28Dec-26	06Jan-27	20Mar-27	29Mar-27	$000	$000	$42068.52	0.00
ML TX0 2 004 CN 10630	Fixation and Installation of Steel Frame for Benches	700	0%	0%	28Dec-26	04Jan-27	20Mar-27	27Mar-27	$000	$000	$17276.03	0.00
ML TX0 2 004 CN 10640	Fixation and Installation of Benches	700	0%	0%	05Jan-27	12Jan-27	28Mar-27	04Apr-27	$000	$000	$40310.72	0.00
ML TX0 2 004 CN 10650	Fixation and Installation of Precast Concrete Seats (Rectangular)	700	0%	0%	05Jan-27	12Jan-27	28Mar-27	04Apr-27	$000	$000	$43680.00	0.00
ML TX0 2 004 CN 10660	Fixation and Installation of Precast Concrete Seats (Circular)	800	0%	0%	05Jan-27	13Jan-27	28Mar-27	05Apr-27	$000	$000	$17160.00	0.00
ML TX0 2 004 CN 10670	Fixation and Installation of Precast Concrete Trash Bins	900	0%	0%	14Jan-27	24Jan-27	06Apr-27	15Apr-27	$000	$000	$14625.00	0.00
ML TX0 2 004 CN 11800	Installingof SiteLightPoles	1100	0%	92%	07Jan-27	19Jan-27	01Oct-26A	29Mar-27	$000	$431,67588	$472,47379	-1300
TOILET/SERVICEBUILDING		5900	9578%	0%	19Jul-26	02Nov-26	27Oct-26	03Jan-27	$ 681,42591	$000	$731,51163	3200
MECHANICAL WORK		4800	100%	0%	03Sep-26	20Oct-26	27Oct-26	21Dec-26	$ 259,92188	$000	$279,92188	-8.00
HVAC SYSTEM		4800	100%	0%	19Sep-26	20Oct-26	27Oct-26	21Dec-26	$18,525.00	$000	$18525.00	-2100
ML TX0 2 004 CN 11500	Install and Finish HVAC andVentilation Works Including Split Air Units	600	100%	0%	14Oct-26	20Oct-26	15Dec-26	21Dec-26	$14,625.00	$000	$14625.00	0.00
ML TX0 2 004 CN 11490	Exhaust,Air Duds Installation withall Accessories	800	100%	0%	19Sep-26	28Sep-26	27Oct-26	04Nov-26	$3900.00	$000	$3900.00	0.00
WATER SUPPLY SYSTEM		3900	100%	0%	07Sep-26	10Oct-26	27Oct-26	10Dec-26	$ 253,50500	$000	$205,50500	-1100
ML TX0 2 004 CN 11580	Installingof HDPE Pipes andValves for Water Supply Network	300	100%	0%	09Sep-26	12Sep-26	29Oct-26	01Nov-26	$39,000.00	$000	$39000.00	0.00
ML TX0 2 004 CN 11550	Installingof Booster Rmp Units Indudingfittings andaccessories	700	100%	0%	29Sep-26	06Oct-26	08Nov-26	15Nov-26	$51,000.00	$000	$51000.00	0.00
ML TX0 2 004 CN 11560	Installingof GRPTanks	800	100%	0%	19Sep-26	28Sep-26	29Oct-26	07Nov-26	$ 104,00000	$000	$104,00000	0.00
ML TX0 2 004 CN 11520	Installingof Valves and Fittings	200	100%	0%	07Sep-26	08Sep-26	27Oct-26	28Oct-26	$9750.00	$000	$9750.00	0.00
ML TX0 2 004 CN 11650	Installingof Water Heater	400	100%	0%	06Oct-26	10Oct-26	07Dec-26	10Dec-26	$1755.00	$000	$1755.00	0.00
SEWERDRANAGESYSTEM		4400	100%	0%	03Sep-26	15Oct-26	27Oct-26	16Dec-26	$53,941.88	$000	$53941.88	-8.00
ML TX0 2 004 CN 11600	Installingof Plumping Rxtures andAccessories	200	100%	0%	19Sep-26	26Sep-26	21Nov-26	22Nov-26	$10,359.38	$000	$10359.38	0.00
ML TX0 2 004 CN 11650	InstallingInspection Chamber for SavageNetwork	900	100%	0%	03Sep-26	13Sep-26	27Oct-26	05Nov-26	$12,187.50	$000	$12187.50	0.00
ML TX0 2 004 CN 11870	Installingof Toilet Fixtures and Accessories Sich asClosets and Basins	900	100%	0%	06Oct-26	15Oct-26	07Dec-26	16Dec-26	$31,395.00	$000	$31395.00	0.00
FIRE PROTECTION		400	100%	0%	17Oct-26	20Oct-26	17Dec-26	21Dec-26	$1950.00	$000	$1950.00	0.00
ML TX0 2 004 CN 11620	Installingof FireFighting Extinguisher and accessoires (PIE-1, PIE-2)	400	100%	0%	17Oct-26	20Oct-26	17Dec-26	21Dec-26	$1950.00	$000	$1950.00	0.00
ELECTRICAL WORKS		1000	100%	0%	14Oct-26	25Oct-26	15Dec-26	26Dec-26	$ 227,64375	$000	$227,64375	0.00
FIXTURE WORKS		1000	100%	0%	14Oct-26	25Oct-26	15Dec-26	26Dec-26	$ 227,64375	$000	$227,64375	0.00
ML TX0 2 004 CN 11780	Installingof Fireautomation and Fie AlarmSystem	400	100%	0%	21Oct-26	25Oct-26	22Dec-26	26Dec-26	$34,320.00	$000	$34320.00	0.00
ML TX0 2 004 CN 11740	Installingand finish Works of Panel Boards	1000	100%	0%	14Oct-26	25Oct-26	15Dec-26	26Dec-26	$84,075.00	$000	$84075.00	0.00
ML TX0 2 004 CN 11650	Installingand finalizeWorksof Sockets and Power Points	400	100%	0%	17Oct-26	20Oct-26	17Dec-26	21Dec-26	$13,846.37	$000	$13846.37	0.00
ML TX0 2 004 CN 11790	Installingand finalizeWorksof Lighting Works including Light Fixtures	400	100%	0%	17Oct-26	20Oct-26	17Dec-26	21Dec-26	$16,050.06	$000	$16050.06	0.00
ML TX0 2 004 CN 11750	InstallingData and Telecommunication System withall Accessories	400	100%	0%	17Oct-26	20Oct-26	17Dec-26	21Dec-26	$18,427.50	$000	$18427.50	0.00
ML TX0 2 004 CN 11680	Installingand finalizeWorksof Security and Access Control System	600	100%	0%	14Oct-26	20Oct-26	15Dec-26	21Dec-26	$22,899.83	$000	$22899.83	0.00
ML TX0 2 004 CN 11770	Installingand finalizeWorksof Earthing Works	600	100%	0%	14Oct-26	20Oct-26	15Dec-26	21Dec-26	$23,400.00	$000	$23400.00	0.00
ML TX0 2 004 CN 11820	Installingand finalizeWorksof LightningProtection System	600	100%	0%	14Oct-26	20Oct-26	15Dec-26	21Dec-26	$14,625.00	$000	$14625.00	0.00
DOORS/WINDOWS		5900	5592%	0%	19Aug-26	02Nov-26	27Oct-26	03Jan-27	$38,164.25	$000	$68250.00	5.00
MLTX02-006-CN-11110	PreliminaryWorks for Doors	300	100%	0%	19Aug-26	22Aug-26	27Oct-26	29Oct-26	$3900.00	$000	$3900.00	0.00
MLTX02-006-CN-11120	Finalize Metal Doors forToilets Building	700	100%	0%	18Oct-26	25Oct-26	15Dec-26	22Dec-26	$5850.00	$000	$5850.00	0.00
MLTX02-006-CN-11130	Finalize Gazzed Curtain WallWorks	700	1429%	0%	26Oct-26	02Nov-26	27Dec-26	03Jan-27	$5014.25	$000	$35100.00	0.00
MLTX02-006-CN-11100	PreliminaryWorks for Windows/CurtainWall	200	100%	0%	19Aug-26	20Aug-26	07Nov-26	08Nov-26	$23,400.00	$000	$23400.00	0.00
METAL WORKS		1000	100%	0%	19Jul-26	29Jul-26	27Oct-26	07Nov-26	$3900.00	$000	$3900.00	0.00
MLTX02-006-CN-11160	Installation of ID Cove for Tank	1000	100%	0%	19Jul-26	29Jul-26	27Oct-26	07Nov-26	$3900.00	$000	$3900.00	0.00
FINISHINGWORKS		4500	100%	0%	07Sep-26	17Oct-26	27Oct-26	17Dec-26	$94,795.00	$000	$94795.00	-1100
FLOR FINISHES		3400	100%	0%	07Sep-26	17Oct-26	09Nov-26	17Dec-26	$37,160.00	$000	$37160.00	0.00
ML TX0 2 004 CN 11220	Ceramic Tiles Floor Finish Works	200	100%	0%	07Sep-26	08Sep-26	09Nov-26	10Nov-26	$11,895.00	$000	$11895.00	0.00
ML TX0 2 004 CN 11210	Granite Tiles Floor Finish Works	400	100%	0%	09Sep-26	13Sep-26	11Nov-26	15Nov-26	$2925.00	$000	$2925.00	0.00
ML TX0 2 004 CN 11220	Epoxy Cast on Concrete Floor	300	100%	0%	14Oct-26	17Oct-26	15Dec-26	17Dec-26	$1170.00	$000	$1170.00	0.00
ML TX0 2 004 CN 11230	Ceramic Skirting Tiles FinishWorks	400	100%	0%	14Sep-26	17Sep-26	16Nov-26	19Nov-26	$1170.00	$000	$1170.00	0.00
WALL FINISHES		4400	100%	0%	13Sep-26	15Oct-26	27Oct-26	16Dec-26	$68,459.00	$000	$64454.00	-1600
ML TX0 2 004 CN 11200	Painting FinishWorks for External Walls	700	100%	0%	13Sep-26	20Sep-26	02Nov-26	09Nov-26	$10,478.00	$000	$10478.00	0.00
ML TX0 2 004 CN 11320	PhenolicPartitions forToilets	700	100%	0%	28Sep-26	05Oct-26	29Nov-26	06Dec-26	$31,200.00	$000	$31200.00	0.00
ML TX0 2 004 CN 11250	Glass Partitionsincluding al accessories anddoors	700	100%	0%	06Oct-26	13Oct-26	07Dec-26	14Dec-26	$12,285.00	$000	$12285.00	0.00
ML TX0 2 004 CN 11270	Granite Coppingfor Papet	200	100%	0%	16Sep-26	17Sep-26	27Oct-26	28Oct-26	$8151.00	$000	$8151.00	0.00
ML TX0 2 004 CN 11840	Painting FinishWorks for Internal Walls	200	100%	0%	14Oct-26	15Oct-26	15Dec-26	16Dec-26	$2340.00	$000	$2340.00	0.00
CEILING FINISHES		1000	100%	0%	07Sep-26	30Sep-26	27Oct-26	07Nov-26	$13,182.00	$000	$13182.00	1000
ML TX0 2 004 CN 11350	Painting FinishWorks for Ceiling	300	100%	0%	28Sep-26	30Sep-26	04Nov-26	07Nov-26	$1638.00	$000	$1638.00	0.00
ML TX0 2 004 CN 11360	Gypsum Board Suspended Ceiling Finish Works For Ceiling	700	100%	0%	19Sep-26	27Sep-26	27Oct-26	03Nov-26	$6926.40	$000	$6926.40	0.00
ML TX0 2 004 CN 11340	PreliminaryWorks for Ceiling PaintingWorks	300	100%	0%	07Sep-26	09Sep-26	27Oct-26	29Oct-26	$4617.66	$000	$4617.66	0.00
SPECIALTIES WORK		1500	100%	0%	21Sep-26	05Oct-26	27Nov-26	09Dec-26	$3,000.00	$000	$30000.00	0.00
MLTX02-006-CN-11390	Sanitary Rxtures andAccessoriesWorks	500	100%	0%	21Sep-26	27Sep-26	23Nov-26	28Nov-26	$14,625.00	$000	$14625.00	0.00
MLTX02-006-CN-11380	Installation of Phenolic Locker	300	100%	0%	06Oct-26	08Oct-26	07Dec-26	09Dec-26	$2437.50	$000	$24375.00	0.00
TESTING & COMMISSIONING		6400	0%	0%	05Nov-26	12Jan-27	30Jan-27	18Apr-27	$000	$000	$000	-5.00
MLTX02-006-TC-11860	Testing and Commissioning forMEP Works for Playground Area	1000	0%	0%	02Jan-27	12Jan-27	07Apr-27	18Apr-27	$000	$000	$000	0.00
MLTX02-006-TC-11870	Testing and Commissioning forMEP Works for Toilet/Service Building	2200	0%	0%	05Nov-26	30Nov-26	30Jan-27	24Feb-27	$000	$000	$000	0.00
MLTX02-006-TC-11880	Testing and Commissioning forMEP Works for landscape Works	2200	0%	0%	01Dec-26	26Dec-26	25Feb-27	25Mar-27	$000	$000	$000	0.00
JAZAN		180.00	2495%	1032%	05Jul-26	25Jan-27	19Aug-26A	19May-27	$2112,538.25	$831,68360	$8467,965.84	-5200
ENGINEERING		1500	0%	0%	05Jul-26	21Jul-26	27Oct-26	12Nov-26	$000	$000	$000	0.00
METHOD STATEMENTS		1500	0%	0%	05Jul-26	21Jul-26	27Oct-26	12Nov-26	$000	$000	$000	0.00
METHOD STATEMENT SUBMITTAL		500	0%	0%	05Jul-26	09Jul-26	27Oct-26	01Nov-26	$000	$000	$000	0.00
ARCHITECTURE WORKS		500	0%	0%	05Jul-26	09Jul-26	27Oct-26	01Nov-26	$000	$000	$000	0.00
ML TX0 2 004 EN 1065	Preparation & Submission of Method Statement for Rence Works	500	100%	0%	05Jul-26	09Jul-26	27Oct-26	01Nov-26	$000	$000	$000	0.00
METHOD STATEMENT APPROVAL		1000	0%	0%	11Jul-26	21Jul-26	02Nov-26	12Nov-26	$000	$000	$000	0.00
ARCHITECTURE WORKS		1000	0%	0%	11Jul-26	21Jul-26	02Nov-26	12Nov-26	$000	$000	$000	0.00
ML TX0 2 004 EN 11220	Approvalof Method Statement for Fence Works	1000	100%	0%	11Jul-26	21Jul-26	02Nov-26	12Nov-26	$000	$000	$000	0.00
PREQUALIFICATION & MATERIAL		700	0%	0%	05Jul-26	12Jul-26	27Oct-26	03Nov-26	$000	$000	$000	0.00

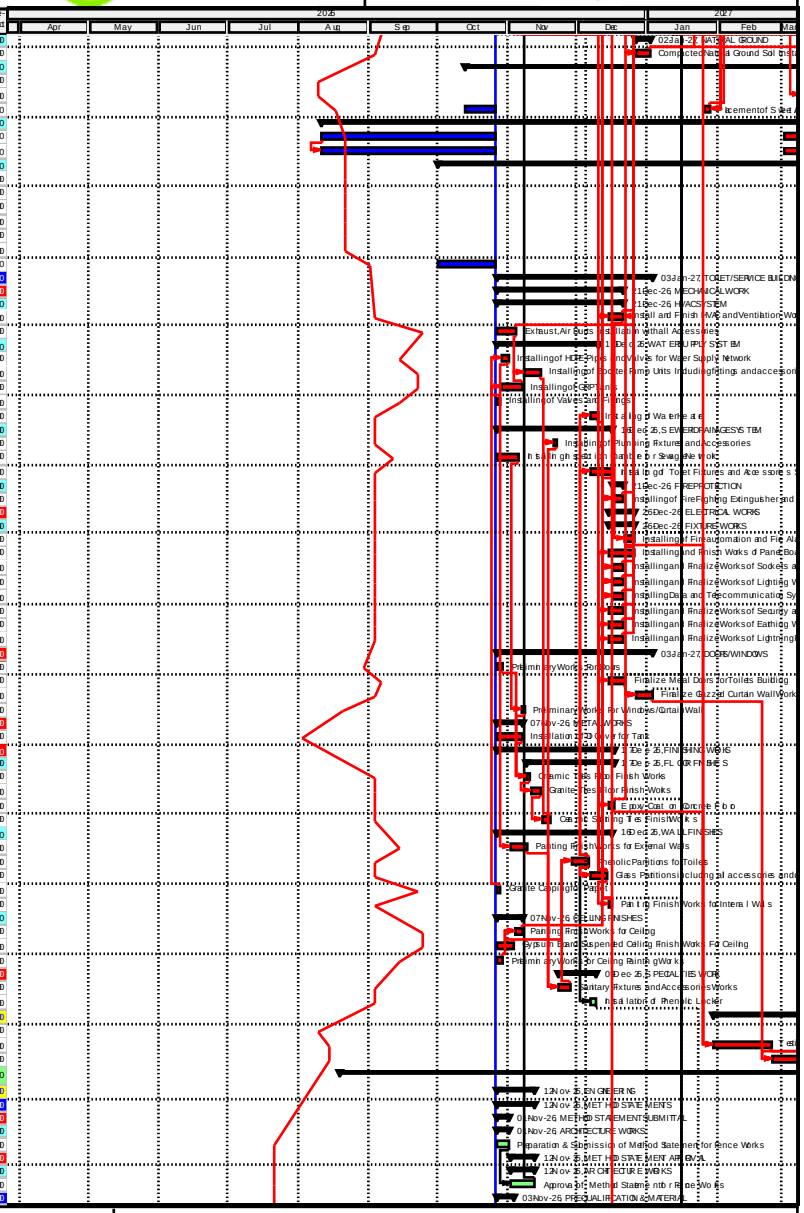

Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work


TASK filter: Remaining work

© Oracle Corporation

MLTX-02-004 - Playground Initiative for Western Region (Asir-Jazan -Jeddah)

Remaining work
D.D 26-10-2026

Activity ID	Activity Name	Original Duration	Schedule %	Performance % Complete	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Variance - BL Project
MATERIAL SUBMITTAL		7 d	0%	0%	05Jul-26	12Jul-26	27Oct-26	03Nov-26	$000	$000	$000	0.d
PLAYGROUND WORKS		7 d	0%	0%	05Jul-26	12Jul-26	27Oct-26	03Nov-26	$000	$000	$000	0.d
PVC MEMBRANE		7 d	0%	0%	05Jul-26	12Jul-26	27Oct-26	03Nov-26	$000	$000	$000	0.d
MLTX02-004-EN-5570	Material Approval for PVC Membrane	7 d	100%	0%	05Jul-26	12Jul-26	27Oct-26	03Nov-26	$000	$000	$000	0.d
STEEL TENSION CABLES		7 d	0%	0%	05Jul-26	12Jul-26	27Oct-26	03Nov-26	$000	$000	$000	0.d
MLTX02-004-EN-5880	Material Approval for Steel Tension Cables	7 d	100%	0%	05Jul-26	12Jul-26	27Oct-26	03Nov-26	$000	$000	$000	0.d
EMERGENCY DOORS		7 d	0%	0%	05Jul-26	12Jul-26	27Oct-26	03Nov-26	$000	$000	$000	0.d
MLTX02-004-EN-5890	Material Approval for Emergency Doors	7 d	100%	0%	05Jul-26	12Jul-26	27Oct-26	03Nov-26	$000	$000	$000	0.d
AIR LOCK DOORS		7 d	0%	0%	05Jul-26	12Jul-26	27Oct-26	03Nov-26	$000	$000	$000	0.d
MLTX02-004-EN-5910	Material Approval for Lock Doors	7 d	100%	0%	05Jul-26	12Jul-26	27Oct-26	03Nov-26	$000	$000	$000	0.d
PADEL WIREMESH/STEEL SETS		7 d	0%	0%	05Jul-26	12Jul-26	27Oct-26	03Nov-26	$000	$000	$000	0.d
MLTX02-004-EN-5950	Material Approval for WireMesh/Steel Sets	7 d	100%	0%	05Jul-26	12Jul-26	27Oct-26	03Nov-26	$000	$000	$000	0.d
PROCUREMENT		107.00	0%	0%	05Jul-26	07Nov-26	27Oct-26	01Mar-27	$000	$000	$000	0.d
SHORT LEAD ITEM		6800	0%	0%	05Jul-26	21Oct-26	27Oct-26	13Jan-27	$000	$000	$000	2500
TOILET/SERVICE WORKS		2000	0%	0%	11Jul-26	24Sep-26	27Oct-26	18Nov-26	$000	$000	$000	4500
PACKAGE AC UNITS		1000	0%	0%	30Jul-26	10Aug-26	27Oct-26	07Nov-26	$000	$000	$000	0.d
ML TX0 2-004 PR 10380	Material Delivery for Package AC Units	1000	100%	0%	30Jul-26	10Aug-26	27Oct-26	07Nov-26	$000	$000	$000	0.d
LIGHTING FIXTURES		1500	0%	0%	06Aug-26	23Aug-26	27Oct-26	12Nov-26	$000	$000	$000	0.d
ML TX0 2-004 PR 10300	Material Delivery for Lighting Fixtures	1500	100%	0%	06Aug-26	23Aug-26	27Oct-26	12Nov-26	$000	$000	$000	0.d
DISTRIBUTION PANELS		1500	0%	0%	11Jul-26	27Jul-26	27Oct-26	12Nov-26	$000	$000	$000	0.d
ML TX0 2-004 PR 10340	Material Delivery for Distribution Panels	1500	100%	0%	11Jul-26	27Jul-26	27Oct-26	12Nov-26	$000	$000	$000	0.d
FURNITURES		2000	0%	0%	01Sep-26	24Sep-26	27Oct-26	18Nov-26	$000	$000	$000	0.d
ML TX0 2-004 PR 10310	Material Delivery for Furnitures	2000	100%	0%	01Sep-26	24Sep-26	27Oct-26	18Nov-26	$000	$000	$000	0.d
PLAYGROUND WORKS		6800	0%	0%	05Jul-26	21Oct-26	27Oct-26	13Jan-27	$000	$000	$000	2500
PVC MEMBRANE		4 d	0%	0%	05Jul-26	08Jul-26	27Oct-26	31Oct-26	$000	$000	$000	0.d
ML TX0 2-004 PR 10540	Material Delivery for PVC Membrane	4 d	100%	0%	05Jul-26	08Jul-26	27Oct-26	31Oct-26	$000	$000	$000	0.d
ARTIFICIAL TURF		1200	0%	0%	09Jul-26	22Jul-26	01Nov-26	14Nov-26	$000	$000	$000	0.d
ML TX0 2-004 PR 10780	Material Delivery for Artificial TURF	1200	100%	0%	09Jul-26	22Jul-26	01Nov-26	14Nov-26	$000	$000	$000	0.d
RUBBER GRANULES		1200	0%	0%	23Jul-26	05Aug-26	15Nov-26	28Nov-26	$000	$000	$000	0.d
ML TX0 2-004 PR 10600	Material Delivery for Rubber Granules	1200	100%	0%	23Jul-26	05Aug-26	15Nov-26	28Nov-26	$000	$000	$000	0.d
PADEL GLASS		1800	0%	0%	06Aug-26	26Aug-26	29Nov-26	19Dec-26	$000	$000	$000	0.d
ML TX0 2-004 PR 10820	Material Delivery for Padel Glass	1800	100%	0%	06Aug-26	26Aug-26	29Nov-26	19Dec-26	$000	$000	$000	0.d
PADEL WIREMESH/STEEL SETS		1500	0%	0%	27Aug-26	13Sep-26	20Dec-26	05Jan-27	$000	$000	$000	0.d
ML TX0 2-004 PR 10840	Material Delivery for WireMesh/Steel Sets	1500	100%	0%	27Aug-26	13Sep-26	20Dec-26	05Jan-27	$000	$000	$000	0.d
INTERLOCKING PAVING		7 d	0%	0%	14Sep-26	21Sep-26	06Jan-27	13Jan-27	$000	$000	$000	0.d
ML TX0 2-004 PR 10380	Material Delivery for Interlocking Block Pavers	7 d	100%	0%	14Sep-26	21Sep-26	06Jan-27	13Jan-27	$000	$000	$000	0.d
MARKING PAINT		7 d	0%	0%	12Jul-26	19Jul-26	27Oct-26	03Nov-26	$000	$000	$000	0.d
ML TX0 2-004 PR 10360	Material Delivery for Marking Paint	7 d	100%	0%	12Jul-26	19Jul-26	27Oct-26	03Nov-26	$000	$000	$000	0.d
PACKAGE AC UNITS		1500	0%	0%	20Jul-26	05Aug-26	04Nov-26	21Nov-26	$000	$000	$000	0.d
ML TX0 2-004 PR 10460	Material Delivery for Package AC Units	1500	100%	0%	20Jul-26	05Aug-26	04Nov-26	21Nov-26	$000	$000	$000	0.d
DISTRIBUTION BOARDS		1500	0%	0%	11Jul-26	27Jul-26	27Oct-26	12Nov-26	$000	$000	$000	0.d
ML TX0 2-004 PR 10640	Material Delivery for Distribution Boards	1500	100%	0%	11Jul-26	27Jul-26	27Oct-26	12Nov-26	$000	$000	$000	0.d
POWER CABLES		1000	0%	0%	03Aug-26	13Aug-26	27Oct-26	07Nov-26	$000	$000	$000	0.d
ML TX0 2-004 PR 10660	Material Delivery for Power Cables	1000	100%	0%	03Aug-26	13Aug-26	27Oct-26	07Nov-26	$000	$000	$000	0.d
LIGHT FIXTURES		2100	0%	0%	15Aug-26	07Sep-26	08Nov-26	01Dec-26	$000	$000	$000	0.d
ML TX0 2-004 PR 10670	PO for Light Fixtures	5 d0	100%	0%	15Aug-26	19Aug-26	08Nov-26	12Nov-26	$000	$000	$000	0.d
ML TX0 2-004 PR 10680	Material Delivery for Light Fixtures	1600	100%	0%	20Aug-26	07Sep-26	14Nov-26	01Dec-26	$000	$000	$000	0.d
CCTV MATERIALS		3000	0%	0%	08Sep-26	21Oct-26	02Dec-26	05Jan-27	$000	$000	$000	7.d
ML TX0 2-004 PR 10690	PO for CCTV	1000	100%	0%	08Sep-26	19Sep-26	02Dec-26	13Dec-26	$000	$000	$000	0.d
ML TX0 2-004 PR 10700	Material Delivery for CCTV	2000	100%	0%	29Sep-26	21Oct-26	14Dec-26	05Jan-27	$000	$000	$000	0.d
POWER OUTLETS/SWITCHES		2100	0%	0%	20Sep-26	14Oct-26	14Dec-26	06Jan-27	$000	$000	$000	0.d
ML TX0 2-004 PR 10710	PO for Power Outlets/Switches	6 d0	100%	0%	20Sep-26	27Sep-26	14Dec-26	20Dec-26	$000	$000	$000	0.d
ML TX0 2-004 PR 10720	Material Delivery for Power Outlets/Switches	1500	100%	0%	28Sep-26	14Oct-26	21Dec-26	06Jan-27	$000	$000	$000	0.d
LANDSCAPE WORKS		3000	0%	0%	05Jul-26	14Sep-26	27Oct-26	30Nov-26	$000	$000	$000	3200
INTERLOCKING PAVING		1000	0%	0%	05Jul-26	15Jul-26	27Oct-26	07Nov-26	$000	$000	$000	0.d
ML TX0 2-004 PR 10750	Material Delivery for Interlocking Block Pavers	1000	100%	0%	05Jul-26	15Jul-26	27Oct-26	07Nov-26	$000	$000	$000	0.d
CUBSTORE		1000	0%	0%	05Jul-26	15Jul-26	27Oct-26	07Nov-26	$000	$000	$000	0.d
ML TX0 2-004 PR 10900	Material Delivery for Cubstore	1000	100%	0%	05Jul-26	15Jul-26	27Oct-26	07Nov-26	$000	$000	$000	0.d
PAVEMENT MARKING		1000	0%	0%	22Jul-26	02Aug-26	27Oct-26	07Nov-26	$000	$000	$000	0.d
ML TX0 2-004 PR 10350	Material Delivery for Pavement Marking	1000	100%	0%	22Jul-26	02Aug-26	27Oct-26	07Nov-26	$000	$000	$000	0.d
TRAFFIC SIGNS		9 d0	0%	0%	09Aug-26	18Aug-26	27Oct-26	05Nov-26	$000	$000	$000	0.d
ML TX0 2-004 PR 10380	Material Delivery for Traffic Signs	9 d0	100%	0%	09Aug-26	18Aug-26	27Oct-26	05Nov-26	$000	$000	$000	0.d
AGRICULTURE SOIL		1200	0%	0%	11Jul-26	23Jul-26	27Oct-26	09Nov-26	$000	$000	$000	0.d
ML TX0 2-004 PR 10850	Material Delivery for Agriculture Soil	1200	100%	0%	11Jul-26	23Jul-26	27Oct-26	09Nov-26	$000	$000	$000	0.d
TRACK SURFACE		1000	0%	0%	25Jul-26	04Aug-26	10Nov-26	21Nov-26	$000	$000	$000	0.d
ML TX0 2-004 PR 10880	Material Delivery for Track Suface	1000	100%	0%	25Jul-26	04Aug-26	10Nov-26	21Nov-26	$000	$000	$000	0.d
GRASS/TREES		1500	0%	0%	11Aug-26	27Aug-26	27Oct-26	12Nov-26	$000	$000	$000	0.d
ML TX0 2-004 PR 10920	Material Delivery for Grass/Trees	1500	100%	0%	11Aug-26	27Aug-26	27Oct-26	12Nov-26	$000	$000	$000	0.d
CABLES		1500	0%	0%	29Aug-26	14Sep-26	14Nov-26	30Nov-26	$000	$000	$000	0.d
ML TX0 2-004 PR 10740	Material Delivery for Cables	1500	100%	0%	29Aug-26	14Sep-26	14Nov-26	30Nov-26	$000	$000	$000	0.d
LONG LEAD ITEM		107.00	0%	0%	13Jul-26	07Nov-26	27Oct-26	01Mar-27	$000	$000	$000	-7.d
PLAYGROUND WORKS		7700	0%	0%	13Jul-26	05Oct-26	27Oct-26	24Jan-27	$000	$000	$000	-4.d
STEEL TENSION CABLES		4700	0%	0%	13Jul-26	05Sep-26	04Nov-26	28Dec-26	$000	$000	$000	0.d
ML TX0 2-004 PR 10560	Material Delivery for Steel Tension Cables	3000	100%	0%	25Jul-26	27Aug-26	16Nov-26	20Dec-26	$000	$000	$000	0.d
ML TX0 2-004 PR 10930	Material Fabrication for Steel Tension Cables	1000	100%	0%	13Jul-26	23Jul-26	04Nov-26	15Nov-26	$000	$000	$000	0.d
ML TX0 2-004 PR 10970	Staging time	7 d0	100%	0%	29Aug-26	05Sep-26	21Dec-26	28Dec-26	$000	$000	$000	0.d
EMERGENCY DOORS		5900	0%	0%	03Aug-26	10Sep-26	27Oct-26	03Jan-27	$000	$000	$000	-2500
ML TX0 2-004 PR 10580	Material Delivery for Emegency Doors	1500	100%	0%	15Aug-26	31Aug-26	08Nov-26	24Nov-26	$000	$000	$000	0.d
ML TX0 2-004 PR 10940	Material Fabrication for Emergency Doors	1000	100%	0%	03Aug-26	13Aug-26	27Oct-26	07Nov-26	$000	$000	$000	0.d
ML TX0 2-004 PR 10980	Staging time	5 d0	100%	0%	06Sep-26	10Sep-26	29Dec-26	03Jan-27	$000	$000	$000	0.d
PRESSURE UNITS		6000	0%	0%	28Jul-26	06Oct-26	27Oct-26	04Jan-27	$000	$000	$000	0.d
ML TX0 2-004 PR 10590	PO for Pressure Units	1000	100%	0%	28Jul-26	08Aug-26	27Oct-26	07Nov-26	$000	$000	$000	0.d
ML TX0 2-004 PR 10600	Material Delivery for Pressure Units	2500	100%	0%	01Sep-26	30Sep-26	01Dec-26	29Dec-26	$000	$000	$000	0.d
ML TX0 2-004 PR 10950	Material Fabrication for Pressure Units	2000	100%	0%	09Aug-26	31Aug-26	08Nov-26	30Nov-26	$000	$000	$000	0.d
ML TX0 2-004 PR 10990	Staging time	5 d0	100%	0%	01Oct-26	06Oct-26	30Dec-26	04Jan-27	$000	$000	$000	0.d
AIR LOCK DOORS		6000	0%	0%	25Jul-26	03Oct-26	16Nov-26	24Jan-27	$000	$000	$000	0.d

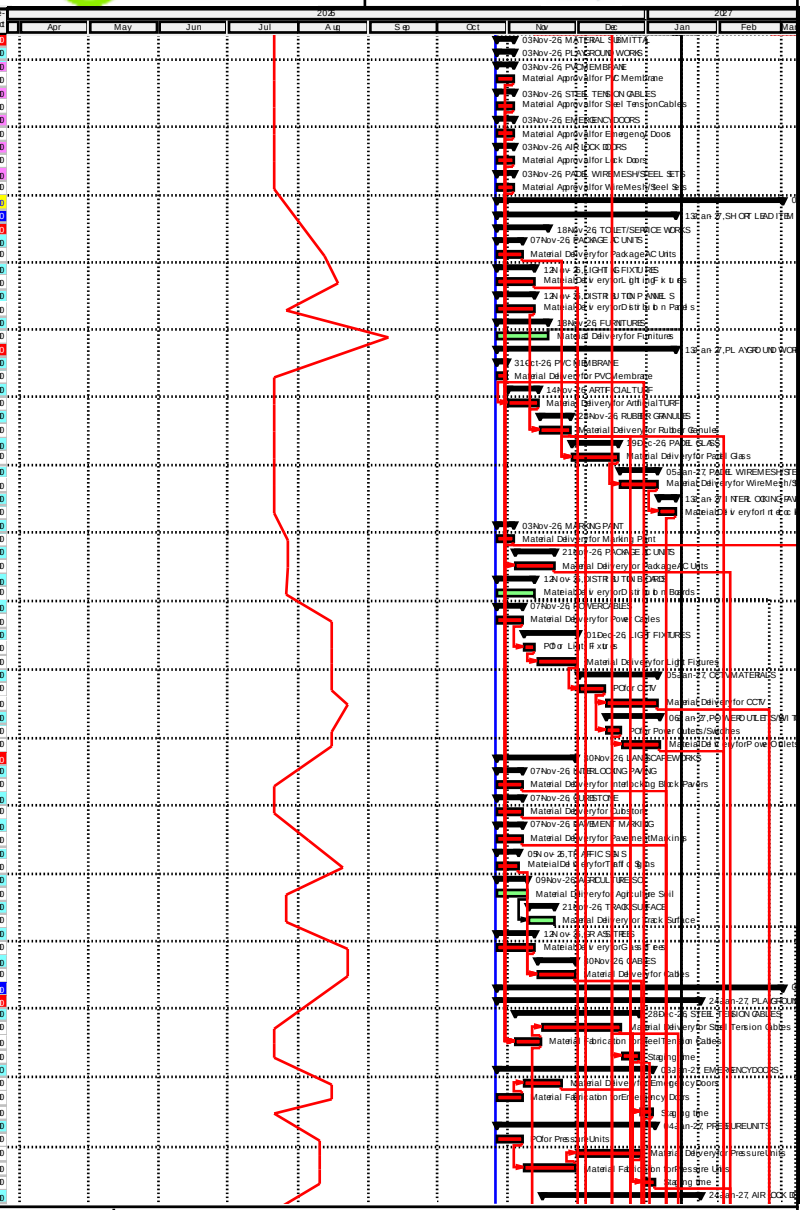

Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work


TASK filter: Remaining work

© Oracle Corporation

MLTX-02-004 - Playground Initiative for Western Region (Asir-Jazan -Jeddah)

Remaining work
D.D 26-10-2026

Activity ID	Activity Name	Original Duration	Schedule %	Performance % Complete	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Variance - BL Project
ML TX0 2-004-PR 1061 0	PCIor Lock Doors	1000	100%	0%	25Jul-26	04Aug-26	16Nov-26	26Nov-26	$000	$000	$000	0.00
ML TX0 2-004-PR 1062 0	Material Deliveryfor Lock Doors	2500	100%	0%	29Aug-26	27Sep-26	21Dec-26	18Jan-27	$000	$000	$000	0.00
ML TX0 2-004-PR 1059 0	Material Fabrication forLock Doors	2000	100%	0%	05Aug-26	27Aug-26	28Nov-26	20Dec-26	$000	$000	$000	0.00
ML TX0 2-004-PR 1100 0	Staging time	5 00	100%	0%	28Sep-26	03Oct-26	19Jan-27	24Jan-27	$000	$000	$000	0.00
LANDSCAPE WORKS		6000	0%	0%	29Aug-26	07Nov-26	21Dec-26	01Mar-27	$000	$000	$000	0.00
LIGHT POLES		6000	0%	0%	29Aug-26	07Nov-26	21Dec-26	01Mar-27	$000	$000	$000	0.00
ML TX0 2-004-PR 1095 0	Material Fabrication forLighting poles	3000	100%	0%	29Aug-26	03Oct-26	21Dec-26	24Jan-27	$000	$000	$000	0.00
ML TX0 2-004-PR 1096 0	Material Deliveryfor Lightingpoles	2500	80%	0%	04Oct-26	01Nov-26	25Jan-27	23Feb-27	$000	$000	$000	0.00
ML TX0 2-004-PR 1101 0	Staging time	5 00	0%	0%	02Nov-26	07Nov-26	24Feb-27	01Mar-27	$000	$000	$000	0.00
CONSTRUCTON PHASE		180 00	2495%	1032%	25Jul-26	25Jan-27	19Aug-26/	19May-27	$2112,513.25	$873,683.60	$8467,965.84	-6900
SITE WORKS		170 00	176%	1034%	25Jul-26	25Jan-27	19Aug-26/	19May-27	$1357,121.74	$797,166.67	$7711,501.33	-6900
LANDSCAPE WORKS		170 00	1782%	1047%	25Jul-26	25Jan-27	19Aug-26/	19May-27	$1357,121.74	$797,166.67	$7614,001.84	-6900
PLAYGROUND AREA		160 00	5623%	2.51%	25Jul-26	16Jan-27	24Oct-26A	06May-27	$ 58,649.49	$26325.00	$1046,922.50	-1400
FOUNDATION LAYERS		120 00	70%	4%	25Jul-26	07Dec-26	24Oct-26A	06Mar-27	$ 201,337.50	$11505.00	$297,625.00	2.00
MLTX02-004-CN-12100	Finishingand SurfaceFinishWorks(Football Playground)	3000	100%	0%	12Sep-26	17Oct-26	04Jan-27	07Feb-27	$ 148,812.50	$000	$148,812.50	0.00
MLTX02-004-CN-12110	Install Sport Equipments- Goal / Nets - (FootballPlayground)	8 00	0%	0%	29Nov-26	07Dec-26	25Feb-27	06Mar-27	$000	$000	$71906.25	0.00
MLTX02-004-CN-12120	Suface Making and Painting(Football Playground)	8 00	0%	0%	29Nov-26	07Dec-26	25Feb-27	06Mar-27	$000	$000	$14381.25	0.00
MLTX02-004-CN-12090	Backfilling andCompaction d BaseLayers (Foolball Playground)	2500	100%	20%	25Jul-26	22Aug-26	24Oct-26A	24Nov-26	$57,525.00	$11505.00	$57525.00	-3.00
PADEL PLAY GROUND		130 00	4103%	6.15%	23Aug-26	22Dec-26	24Oct-26A	12Apr-27	$57,200.00	$8580.00	$139,425.00	-3900
MLTX02-004-CN-12150	Finishingand SurfaceFinishWorks(Padel Playground)	3000	2667%	0%	18Oct-26	21Nov-26	08Feb-27	18Mar-27	$34,300.00	$000	$53625.00	0.00
MLTX02-004-CN-12160	Install Sport Equipments- Goal / Nets - (Padel Playground)	1300	0%	0%	29Nov-26	13Dec-26	20Mar-27	03Apr-27	$000	$000	$32175.00	0.00
MLTX02-004-CN-12170	Suface Making and Painting(Padel Playground)	8 00	0%	0%	14Dec-26	22Dec-26	04Apr-27	12Apr-27	$000	$000	$10725.00	0.00
MLTX02-004-CN-12140	Backfilling andCompaction d BaseLayers (Padel Playground)	2000	100%	20%	23Aug-26	14Sep-26	24Oct-26A	24Nov-26	$42,900.00	$8580.00	$42900.00	-8.00
BASKET BALL PLAY GROUND		9600	2632%	2.22%	15Sep-26	22Dec-26	24Oct-26A	12Apr-27	$33,914.49	$6240.00	$210,180000	-5900
MLTX02-004-CN-12200	Finishingand SurfaceFinishWorks(BasketballPlaygound)	3000	1667%	0%	21Oct-26	24Nov-26	29Dec-26	01Feb-27	$42,714.45	$000	$156,000000	0.00
MLTX02-004-CN-12210	Install Sport Equipments- Goal / Nets - (Basketball Playground)	1000	0%	0%	08Dec-26	19Dec-26	07Mar-27	21Mar-27	$000	$000	$78000.00	0.00
MLTX02-004-CN-12220	Suface Making and Painting(BasketballPlaygound)	8 00	0%	0%	14Dec-26	22Dec-26	04Apr-27	12Apr-27	$000	$000	$15600.00	0.00
MLTX02-004-CN-12190	Backfilling andCompaction d BaseLayers (Basketball Playground)	3000	100%	20%	15Sep-26	20Oct-26	24Oct-26A	30Nov-26	$31,200.00	$6240.00	$31200.00	-3.00
PADEL FENCE		2100	0%	0%	23Dec-26	16Jan-27	13Apr-27	06May-27	$000	$000	$82875.00	0.00
MLTX02-004-CN-12230	Excavation for Fence	3 00	0%	0%	23Dec-26	26Dec-26	13Apr-27	15Apr-27	$000	$000	$8287.50	0.00
MLTX02-004-CN-12240	ConcreteFoundation for Fence indudingPostsFixaiton	4 00	0%	0%	27Dec-26	30Dec-26	17Apr-27	20Apr-27	$000	$000	$16575.00	0.00
MLTX02-004-CN-12250	Tempered Glass Fenc Installation and Fixation	5 00	0%	0%	05Jan-27	10Jan-27	26Apr-27	01May-27	$000	$000	$33150.00	0.00
MLTX02-004-CN-12260	Chain Link Fence Installation andFixaiton	5 00	0%	0%	05Jan-27	10Jan-27	26Apr-27	01May-27	$000	$000	$16575.00	0.00
MLTX02-004-CN-12270	Install ofFenceGates	5 00	0%	0%	11Jan-27	16Jan-27	02May-27	06May-27	$000	$000	$4143.75	0.00
MLTX02-004-CN-12241	Backfilling andReinstatement for ConcreteFoundation	4 00	0%	0%	31Dec-26	04Jan-27	21Apr-27	25Apr-27	$000	$000	$4143.75	0.00
CURBSTONE INTERLOCK		8300	100%	0%	27Sep-26	24Oct-26	27Oct-26	31Jan-27	$ 216,197.50	$000	$215,197.50	-5900
MLTX02-004-CN-11960	Interlockinstallation (Grey Stale)for LandScape (IndudingFinishing Works)	1500	100%	0%	07Oct-26	24Oct-26	14Jan-27	31Jan-27	$ 165,900.00	$000	$165,900.00	0.00
MLTX02-004-CN-12020	ConcreteWorks Under Curbstone	5 00	100%	0%	27Sep-26	01Oct-26	27Oct-26	01Nov-26	$15,990.00	$000	$15990.00	0.00
MLTX02-004-CN-12030	CubstoneInstallation	4 00	100%	0%	03Oct-26	06Oct-26	29Dec-26	02Jan-27	$54,307.50	$000	$54307.50	0.00
AIRDOME		100 00	1136%	1057%	27Sep-26	26Dec-26	24Sep-26/	28Mar-27	$ 580,625.00	$521,381.25	$4933,500.00	-7700
CIVIL WORKS		6500	3333%	31%	27Sep-26	15Nov-26	24Sep-26/	10Feb-27	$ 580,625.00	$521,381.25	$1681,875.00	-7700
MLTX02-004-CN-12310	Install ofMembraneCovering System (Air Dome)	4 00	0%	0%	08Nov-26	11Nov-26	03Feb-27	07Feb-27	$000	$000	$56,625.00	0.00
MLTX02-004-CN-12320	Thermal Insulation Works(Air Dome)	3 00	0%	0%	12Nov-26	15Nov-26	08Feb-27	10Feb-27	$000	$000	$56,625.00	0.00
MLTX02-004-CN-12300	Cable System Installation (AirDome)	3 00	100%	93%	27Sep-26	29Sep-26	24Sep-26/	28Dec-26	$ 580,625.00	$521,381.25	$56,625.00	-7900
MECHANICAL WORKS		1300	0%	0%	16Nov-26	30Nov-26	11Feb-27	27Feb-27	$000	$000	$1121,250.00	0.00
MLTX02-004-CN-12350	AirDuctsand Gills Installation (Air Dome)	1000	0%	0%	16Nov-26	26Nov-26	11Feb-27	23Feb-27	$000	$000	$210,312.50	0.00
MLTX02-004-CN-12360	AirUnits Installation (Air Dome)	1300	0%	0%	16Nov-26	30Nov-26	11Feb-27	27Feb-27	$000	$000	$448,500.00	0.00
MLTX02-004-CN-12370	Exhaust Fans and Ducts Installation (AirDome)	1100	0%	0%	16Nov-26	28Nov-26	11Feb-27	24Feb-27	$000	$000	$392,437.50	0.00
ELECTRICAL WORKS		2200	0%	0%	01Dec-26	26Dec-26	28Feb-27	28Mar-27	$000	$000	$1681,875.00	0.00
MLTX02-004-CN-12380	Light Fixture Works (AirDome)	2000	0%	0%	01Dec-26	23Dec-26	28Feb-27	25Mar-27	$000	$000	$210,312.50	0.00
MLTX02-004-CN-12390	Distribution Board andElectrical Works (Air Dome)	1800	0%	0%	01Dec-26	21Dec-26	28Feb-27	23Mar-27	$000	$000	$210,312.50	0.00
MLTX02-004-CN-12400	External Electrical Comection Works (Air Dome)	2000	0%	0%	01Dec-26	23Dec-26	28Feb-27	25Mar-27	$000	$000	$210,312.50	0.00
MLTX02-004-CN-12410	EmegencyGeneator Installation (Air Dome)	2000	0%	0%	01Dec-26	23Dec-26	28Feb-27	25Mar-27	$000	$000	$560,625.00	0.00
MLTX02-004-CN-12420	Control System Installaton (Air Dome)	2200	0%	0%	01Dec-26	26Dec-26	28Feb-27	28Mar-27	$000	$000	$210,312.50	0.00
FINISHE SWORKS		2500	0%	0%	19Nov-26	17Dec-26	15Feb-27	20Mar-27	$000	$000	$448,500.00	0.00
MLTX02-004-CN-12330	Doors Installation IncludingEmergency, Ettrance doors (AirDome)	1000	0%	0%	19Nov-26	30Nov-26	15Feb-27	27Feb-27	$000	$000	$224,250.00	0.00
MLTX02-004-CN-12340	Logo andSignsInstalation(Air Dome)	1500	0%	0%	01Dec-26	17Dec-26	28Feb-27	20Mar-27	$000	$000	$224,250.00	0.00
IRRIGATION NETWORK		3900	5018%	0%	19Oct-26	01Nov-26	14Dec-26	27Jan-27	$46,475.00	$000	$92625.00	-2700
ML TX0 2-004-CN 13210	Installingof Valves and fittings for Irrigation Network	4 00	100%	0%	19Oct-26	22Oct-26	14Dec-26	17Dec-26	$46,475.00	$000	$46475.00	0.00
ML TX0 2-004-CN 13220	Installingof Bubblersand Sprayes	3 00	0%	0%	29Oct-26	01Nov-26	25Jan-27	27Jan-27	$000	$000	$46150.00	0.00
NATURAL GROUND		5 00	60%	0%	24Oct-26	28Oct-26	19Jan-27	24Jan-27	$48,174.75	$000	$80291.25	0.00
ML TX0 2-004-CN 11990	CompactedNatural Ground Soil InstallationWorks for Lantscape	5 00	60%	0%	24Oct-26	28Oct-26	19Jan-27	24Jan-27	$48,174.75	$000	$80291.25	0.00
PLANTING		2800	0%	0%	02Nov-26	03Dec-26	28Jan-27	02Mar-27	$000	$000	$573,46250	0.00
ML TX0 2-004-CN 12050	Placementof Sweet/Agricultural Soil(Including levelling andGrading)	5 00	0%	0%	02Nov-26	07Nov-26	28Jan-27	02Feb-27	$000	$000	$105,420000	0.00
ML TX0 2-004-CN 12060	Placementof Lawn Ground Cover (Rilling and Compaction)	3 00	0%	0%	01Dec-26	03Dec-26	28Feb-27	02Mar-27	$000	$000	$175,17500	0.00
ML TX0 2-004-CN 12070	Placementand Fkationof Trees	3 00	0%	0%	28Nov-26	30Nov-26	24Feb-27	27Feb-27	$000	$000	$211,867.50	0.00
WALKING/BIKE PATHS		8 00	0%	92%	05Dec-26	13Dec-26	19Aug-26/	02Mar-27	$000	$130,681.66	$142,045.28	-150.00
ML TX0 2-004-CN 12000	Bike PathPrepaationand Installation Wolks	8 00	0%	92%	05Dec-26	13Dec-26	19Aug-26/	02Mar-27	$000	$130,681.66	$142,045.28	-150.00
GENERAL FURNITURE		160 00	1519%	1594%	07Oct-26	25Jan-27	17Oct-26A	19May-27	$ 113,197.50	$118,778.77	$745,154.31	-8300
ML TX0 2-004-CN 11970	Stamped ConcreteWorks for LandScape (IndudingFinishing Works)	8 00	0%	0%	14Dec-26	22Dec-26	27Oct-26	04Nov-26	$000	$000	$140400.00	0.00
ML TX0 2-004-CN 12040	Traffic Signs Posts and Poles Installation	7 00	0%	0%	06Jan-27	13Jan-27	30Mar-27	06Apr-27	$000	$000	$9750.00	0.00
ML TX0 2-004-CN 12440	Fixation and Installaiton of Steel Rame for Benches	1200	0%	0%	14Dec-26	27Dec-26	03Mar-27	20Mar-27	$000	$000	$172276.88	0.00
ML TX0 2-004-CN 12450	Fixation and Installaiton of Benches	8 00	0%	0%	28Dec-26	05Jan-27	21Mar-27	29Mar-27	$000	$000	$40310.72	0.00
ML TX0 2-004-CN 12460	Fixation and Installaiton of Precast Concrete Seats (Rectangular)	8 00	0%	0%	28Dec-26	05Jan-27	21Mar-27	29Mar-27	$000	$000	$43680.00	0.00
ML TX0 2-004-CN 12470	Fixation and Installaiton of Precast Concrete Seats (Circular)	8 00	0%	0%	28Dec-26	05Jan-27	21Mar-27	29Mar-27	$000	$000	$17160.00	0.00
ML TX0 2-004-CN 12480	Fixation and Installaiton of Precast Concrete Trash Bins	8 00	0%	0%	17Jan-27	25Jan-27	08May-27	19May-27	$000	$000	$14625.00	0.00
ML TX0 2-004-CN 12920	PreliminaryWorks for SiteLigh t PolesIncluding Cable and Bases Wolks	1400	100%	0%	07Oct-26	22Oct-26	03Jan-27	18Jan-27	$ 113,197.50	$000	$113,197.50	0.00
ML TX0 2-004-CN 12930	Installingof SiteLightPoles	1100	0%	25%	24Dec-26	05Jan-27	17Oct-26A	25Mar-27	$000	$118,778.77	$475,115.06	-125.00
PARKING		1200	0%	0%	23Dec-26	05Jan-27	05Nov-26	18Nov-26	$000	$000	$97500.40	0.00
MLTX02-004-CN-11940	Interlockinstallation (8 Cm) for Parking Area (IndudingFinishing Works)	7 00	0%	0%	29Dec-26	05Jan-27	11Nov-26	18Nov-26	$000	$000	$68249.02	0.00
MLTX02-004-CN-11950	SitePrepaation& CompactionUnder Interlock for Parking Area	5 00	0%	0%	23Dec-26	28Dec-26	05Nov-26	10Nov-26	$000	$000	$29251.46	0.00
TOILET/SERVICE BUILDING		7700	9986%	1012%	20Aug-26	16Nov-26	15Sep-26/	11Jan-27	$ 251,411.51	$76516.93	$756,464.51	-2600
THERMAL &MOISTER PROTECTION		800	100%	85%	05Sep-26	13Nov-26	29Sep-26/	04Nov-26	$15,601.15	$14116.93	$16608.15	-2400
MLTX02-004-CN-12650	Finalize Water ProofingWorks for Roding and Wet Areas	8 00	100%	85%	05Sep-26	13Sep-26	29Sep-26/	04Nov-26	$15,601.15	$14116.93	$16608.15	-2400

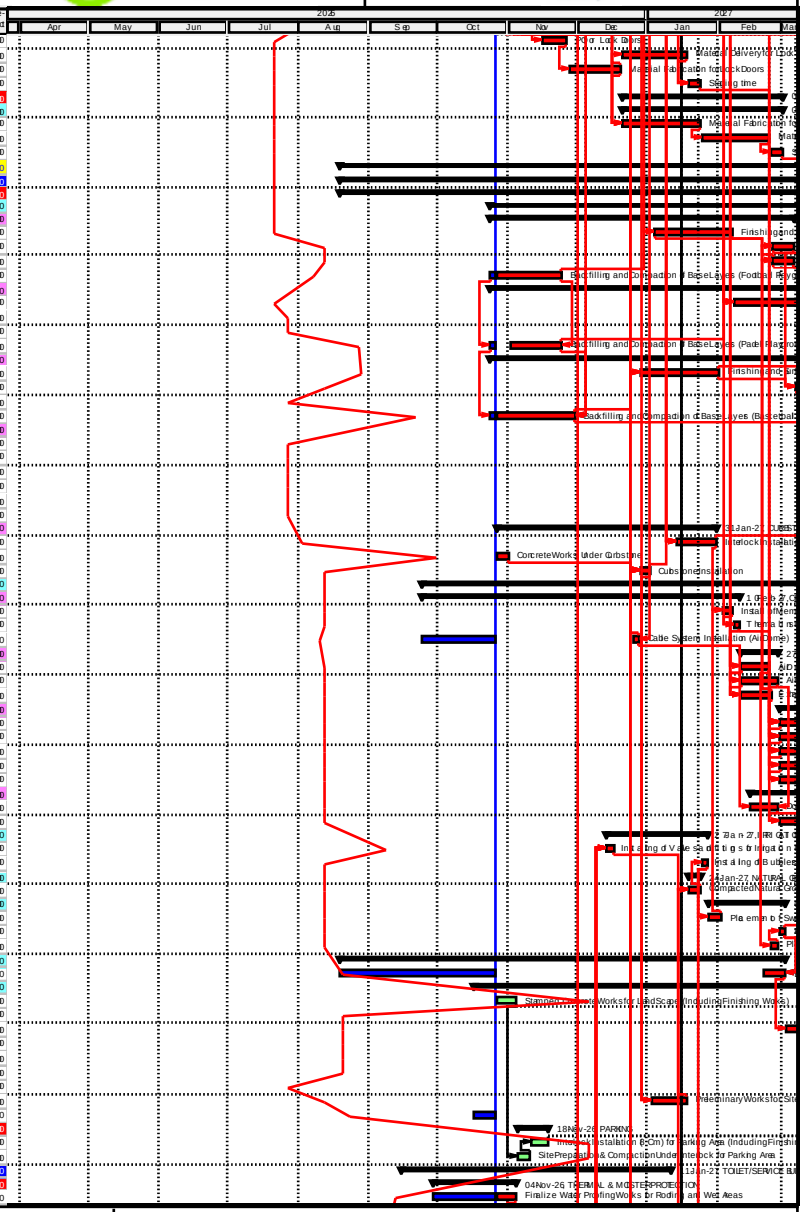

Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work


TASK filter: Remaining work

© Oracle Corporation

MLTX-02-004 - Playground Initiative for Western Region (Asir-Jazan -Jeddah)

Remaining work
D.D 26-10-2026

Activity ID	Activity Name	Original Duration	Schedule %	Performance % Complete	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Variance - BL Project
MECHANICAL WORK		5200	100%	1722%	31Aug-26	18Oct-26	15Sep-26*	13Dec-26	$ 32,333.38	$62400.00	$32,333.38	-3500
HVAC SYSTEM		900	100%	0%	08Oct-26	18Oct-26	03Dec-26	13Dec-26	$14,625.00	$000	$14625.00	0.00
MLTX02-004-CN-12730	Install and Finish HVAC and Ventilation Works Including Split Air Units	900	100%	0%	08Oct-26	18Oct-26	03Dec-26	13Dec-26	$14,625.00	$000	$14625.00	0.00
WATER SUPPLY SYSTEM		4500	100%	3022%	03Sep-26	10Oct-26	15Sep-26*	05Dec-26	$ 26,500.00	$62400.00	$26,500.00	-3800
MLTX02-004-CN-12770	Installing of Booster Pump Units Including fittings and accessories	500	100%	0%	27Sep-26	01Oct-26	08Nov-26	12Nov-26	$91,000.00	$000	$91000.00	0.00
MLTX02-004-CN-13170	Installing of Valves and Fittings	600	100%	0%	03Sep-26	09Sep-26	27Oct-26	02Nov-26	$9750.00	$000	$9750.00	0.00
MLTX02-004-CN-13150	Installing of Water Heater	700	100%	0%	03Oct-26	10Oct-26	28Nov-26	05Dec-26	$1755.00	$000	$1755.00	0.00
MLTX02-004-CN-12780	Installing of GRP Tanks	800	100%	60%	16Sep-26	26Sep-26	15Sep-26*	07Nov-26	$ 104,000.00	$62400.00	$104,000.00	-3700
SEWER/DRAINAGE SYSTEM		3600	100%	0%	31Aug-26	12Oct-26	27Oct-26	07Dec-26	$ 19,254.38	$000	$19,254.38	0.00
MLTX02-004-CN-12600	Installing of Plumping Fixtures and Accessories	200	100%	0%	17Sep-26	19Sep-26	14Nov-26	15Nov-26	$10,359.38	$000	$10359.38	0.00
MLTX02-004-CN-13180	Installing UPVC Pipes for External Connection for Sewage Network	700	100%	0%	09Sep-26	16Sep-26	05Nov-26	12Nov-26	$85,312.50	$000	$85312.50	0.00
MLTX02-004-CN-13250	Installing Inspection Chamber for Sewage Network	800	100%	0%	31Aug-26	08Sep-26	27Oct-26	04Nov-26	$12,187.50	$000	$12187.50	0.00
MLTX02-004-CN-13270	Installing of Toilet Fixtures and Accessories Such as Closets and Basins	900	100%	0%	03Oct-26	12Oct-26	28Nov-26	07Dec-26	$31,395.00	$000	$31395.00	0.00
FIRE PROTECTION		700	100%	0%	11Oct-26	18Oct-26	06Dec-26	13Dec-26	$1950.00	$000	$1950.00	0.00
MLTX02-004-CN-12810	Installing of Fire Fighting Extinguisher and accessories (PIE-1, PIE-2)	700	100%	0%	11Oct-26	18Oct-26	06Dec-26	13Dec-26	$1950.00	$000	$1950.00	0.00
ELECTRICAL WORKS		1400	100%	0%	08Oct-26	24Oct-26	03Dec-26*	19Dec-26	$ 19,397.39	$000	$19,397.39	0.00
FIXTURE WORKS		1400	100%	0%	08Oct-26	24Oct-26	03Dec-26	19Dec-26	$ 19,397.39	$000	$19,397.39	0.00
MLTX02-004-CN-12820	Installing of Fireautomation and Fie Alarm System	500	100%	0%	19Oct-26	24Oct-26	14Dec-26	19Dec-26	$34,320.00	$000	$34320.00	0.00
MLTX02-004-CN-12840	Installing and finish Works of Panel Boards	1000	100%	0%	08Oct-26	19Oct-26	03Dec-26	14Dec-26	$84,075.00	$000	$84075.00	0.00
MLTX02-004-CN-12890	Installing and finalize Works of Lighting Works including Light Fixtures	700	100%	0%	11Oct-26	18Oct-26	06Dec-26	13Dec-26	$16,050.00	$000	$16050.00	0.00
MLTX02-004-CN-12910	Installing Data and Telecommunication System with all Accessories	700	100%	0%	11Oct-26	18Oct-26	06Dec-26	13Dec-26	$18,427.50	$000	$18427.50	0.00
MLTX02-004-CN-12950	Installing and finalize Works of Security and Access Control System	900	100%	0%	08Oct-26	18Oct-26	03Dec-26	13Dec-26	$22,899.83	$000	$22899.83	0.00
MLTX02-004-CN-12970	Installing and finalize Works of Lightning Protection System	900	100%	0%	08Oct-26	18Oct-26	03Dec-26	13Dec-26	$14,625.00	$000	$14625.00	0.00
DOORS/WINDOWS		3700	100%	0%	20Aug-26	13Oct-26	27Oct-26	08Dec-26	$58,500.00	$000	$58500.00	9.00
MLTX02-004-CN-13040	Finalize Gazzed Curtain Wall Works	500	100%	0%	08Oct-26	13Oct-26	03Dec-26	08Dec-26	$35,100.00	$000	$35100.00	0.00
MLTX02-004-CN-13120	Preliminary Works for Windows/Curtain Wall	1200	100%	0%	20Aug-26	02Sep-26	27Oct-26	09Nov-26	$23,400.00	$000	$23400.00	0.00
METAL WORKS		2500	100%	0%	20Aug-26	04Oct-26	27Oct-26	24Nov-26	$13,650.00	$000	$13650.00	-1800
MLTX02-004-CN-12610	Installation of Galvanized Steel Ladder	500	100%	0%	16Sep-26	21Sep-26	08Nov-26	12Nov-26	$5850.00	$000	$5850.00	0.00
MLTX02-004-CN-12980	Installation of Cover for Tank	400	100%	0%	20Aug-26	24Aug-26	27Oct-26	31Oct-26	$3900.00	$000	$3900.00	0.00
MLTX02-004-CN-12990	Installation of Galvanized Steel Roof Scupper	1000	100%	0%	22Sep-26	04Oct-26	14Nov-26	24Nov-26	$3900.00	$000	$3900.00	0.00
FINISHING WORKS		6500	9881%	0%	03Sep-26	15Nov-26	27Oct-26	11Jan-27	$74,523.00	$000	$75674.00	-3.00
FLOOR FINISHES		6600	80%	0%	06Sep-26	16Nov-26	27Oct-26	11Jan-27	$4212.00	$000	$5265.00	-5.00
ML TX02-004-CN-13050	Granite Tiles Floor Finish Works	600	100%	0%	06Sep-26	12Sep-26	27Oct-26	02Nov-26	$2925.00	$000	$2925.00	0.00
ML TX02-004-CN-13060	Epoxy Coat on Concrete Floor	2000	10%	0%	25Oct-26	16Nov-26	20Dec-26	11Jan-27	$ 117.00	$000	$1170.00	0.00
ML TX02-004-CN-13070	Ceramic Skirting Tiles Finish Works	400	100%	0%	13Sep-26	16Sep-26	03Nov-26	07Nov-26	$1170.00	$000	$1170.00	0.00
WALL FINISHES		3400	100%	0%	14Sep-26	10Oct-26	27Oct-26	05Dec-26	$64,454.00	$000	$64454.00	-1200
ML TX02-004-CN-13010	Painting Finish Works for External Walls	300	100%	0%	14Sep-26	16Sep-26	27Oct-26	29Oct-26	$10,478.00	$000	$10478.00	0.00
ML TX02-004-CN-13030	Phenolic Partitions for Toilets	700	100%	0%	24Sep-26	01Oct-26	19Nov-26	26Nov-26	$31,200.00	$000	$31200.00	0.00
ML TX02-004-CN-13140	Glass Partitions including all accessories and doors	500	100%	0%	03Oct-26	07Oct-26	28Nov-26	02Dec-26	$12,285.00	$000	$12285.00	0.00
ML TX02-004-CN-13150	Granite Copping for Papet	200	100%	0%	14Sep-26	15Sep-26	05Nov-26	07Nov-26	$8151.00	$000	$8151.00	0.00
ML TX02-004-CN-13240	Painting Finish Works for Internal Walls	200	100%	0%	08Oct-26	10Oct-26	03Dec-26	05Dec-26	$2340.00	$000	$2340.00	0.00
CEILING FINISHES		2400	100%	0%	03Sep-26	01Oct-26	27Oct-26	23Nov-26	$6255.60	$000	$6255.60	0.00
ML TX02-004-CN-13280	Painting Finish Works for Ceiling	900	100%	0%	21Sep-26	01Oct-26	14Nov-26	23Nov-26	$1638.00	$000	$1638.00	0.00
ML TX02-004-CN-13300	Preliminary Works for Ceiling Painting Works	1500	100%	0%	03Sep-26	20Sep-26	27Oct-26	12Nov-26	$4617.60	$000	$4617.60	0.00
SPECIALTIES WORK		1200	100%	0%	20Sep-26	04Oct-25	16Nov-26	29Nov-26	$39,000.00	$000	$39000.00	0.00
MLTX02-004-CN-12700	Sanitary Fixtures and Accessories Works	300	100%	0%	20Sep-26	22Sep-26	16Nov-26	18Nov-26	$14,625.00	$000	$14625.00	0.00
MLTX02-004-CN-13160	Installation of Phenolic Locker	200	100%	0%	03Oct-26	04Oct-26	28Nov-26	29Nov-26	$24,375.00	$000	$24375.00	0.00
TESTING & COMMISSIONING		6300	0%	0%	17Nov-26	19Jan-27	28Jan-27	15Apr-27	$000	$000	$000	-8.00
MLTX02-004-TC-11890	Testing and Commissioning for MEP Works for Playground Area	1600	0%	0%	27Dec-26	13Jan-27	29Mar-27	15Apr-27	$000	$000	$000	0.00
MLTX02-004-TC-11900	Testing and Commissioning for MEP Works for Toilet/Service Building	2500	0%	0%	17Nov-26	15Dec-26	28Jan-27	27Feb-27	$000	$000	$000	0.00
MLTX02-004-TC-11910	Testing and Commissioning for MEP Works for Landscape Works	500	0%	0%	14Jan-27	19Jan-27	07Apr-27	12Apr-27	$000	$000	$000	0.00
PROJECT CLOSEOUT & DEMOBLIZATION		2800	0%	0%	14Jan-27	25Jan-27	29Mar-27	29Apr-27	$000	$000	$000	-1800
As-Built DWGs		2600	0%	0%	14Jan-27	23Jan-27	29Mar-27	27Apr-27	$000	$000	$000	-1800
As Built DWGs Submittals		2200	0%	0%	14Jan-27	18Jan-27	29Mar-27	22Apr-27	$000	$000	$000	-1800
MLTX02-004-CO-12000	As Built DWGs Submittal for Playground Area Works	400	0%	0%	14Jan-27	18Jan-27	19Apr-27	22Apr-27	$000	$000	$000	0.00
MLTX02-004-CO-12010	As Built DWGs Submittal for Toilet/Service Building Works	400	0%	0%	14Jan-27	18Jan-27	29Mar-27	01Apr-27	$000	$000	$000	0.00
MLTX02-004-CO-12020	As Built DWGs Submittal for Landscape Works	400	0%	0%	14Jan-27	18Jan-27	07Apr-27	11Apr-27	$000	$000	$000	0.00
As Built DWGs Approvals		2200	0%	0%	19Jan-27	23Jan-27	03Apr-27	27Apr-27	$000	$000	$000	-1800
MLTX02-004-CO-12040	As Built DWGs Approval for Playground Area Works	400	0%	0%	19Jan-27	23Jan-27	24Apr-27	27Apr-27	$000	$000	$000	0.00
MLTX02-004-CO-12050	As Built DWGs Approval for Toilet/Service Building Works	400	0%	0%	19Jan-27	23Jan-27	03Apr-27	06Apr-27	$000	$000	$000	0.00
MLTX02-004-CO-12060	As Built DWGs Approval for Landscape Works	400	0%	0%	19Jan-27	23Jan-27	12Apr-27	15Apr-27	$000	$000	$000	0.00
Demobilization		600	0%	0%	19Jan-27	25Jan-27	24Apr-27	29Apr-27	$000	$000	$000	0.00
MLTX02-004-CO-12080	Demobilization of Manpower	200	0%	0%	19Jan-27	20Jan-27	24Apr-27	25Apr-27	$000	$000	$000	0.00
MLTX02-004-CO-12090	Removal of Equipment from Site	200	0%	0%	19Jan-27	20Jan-27	24Apr-27	25Apr-27	$000	$000	$000	0.00
MLTX02-004-CO-12100	Site Clean Up	200	0%	0%	21Jan-27	23Jan-27	26Apr-27	27Apr-27	$000	$000	$000	0.00
MLTX02-004-CO-12110	Restoration of Ground Surfaces	200	0%	0%	24Jan-27	25Jan-27	28Apr-27	29Apr-27	$000	$000	$000	0.00

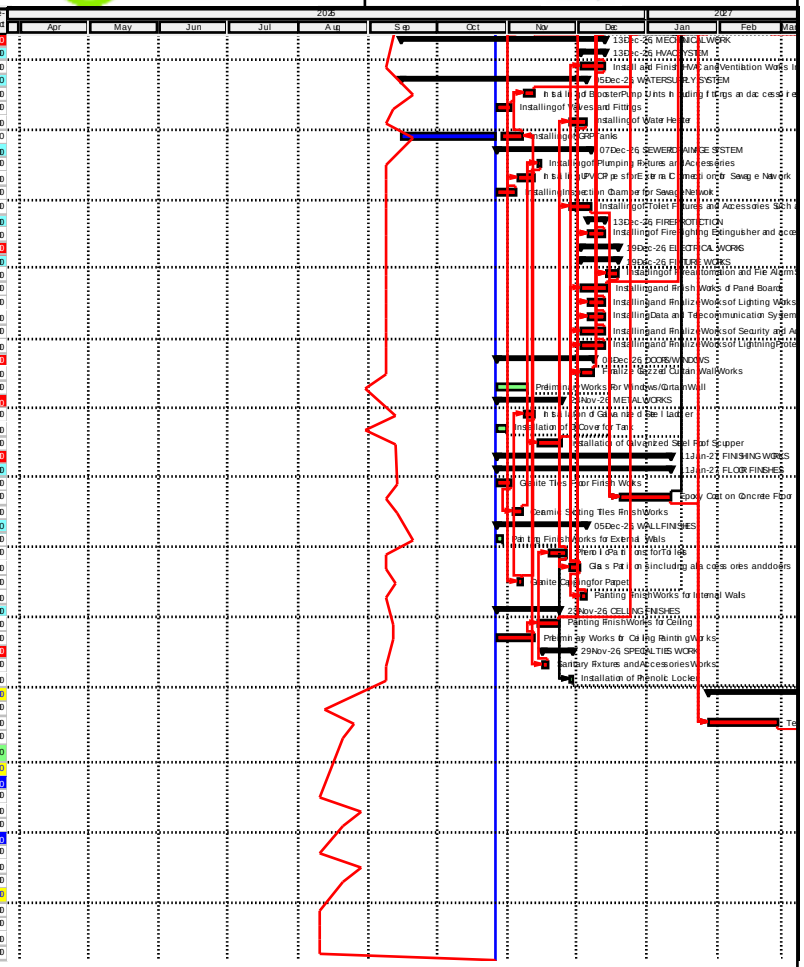

Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work

TASK filter: Remaining work

© Oracle Corporation
