
PLAYGROUNDS INITIATIVE - QASSIM, HAIL & TABUK - 25-Oct-2026

Activity ID	Activity Name	O.D	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Schedule % Complete	Performance % Complete	Variance - BL Project Duration
PLAYGROUNDS INITIATIVE - QASSIM, HAIL & TABUK - 25-Oct-2026		301	17-Feb-26 08:00	16-Dec-26 17:00	17-Feb-26 08:00 A	14-Feb-27 15:24	29,430,559.83	24,884,521.11	35,709,993.00	82.42%	69.69%	-51
MILESTONES		301	17-Feb-26 08:00	16-Dec-26 17:00	17-Feb-26 08:00 A	14-Feb-27 15:24	0.00	0.00	0.00	0%	0%	-51
GENERAL MILESTONES		301	17-Feb-26 08:00	16-Dec-26 17:00	17-Feb-26 08:00 A	14-Feb-27 15:24	0.00	0.00	0.00	0%	0%	-51
CONTRACUAL MILESTONES		239	05-May-26 17:00	16-Dec-26 17:00	05-May-26 17:00 A	14-Feb-27 15:24	0.00	0.00	0.00	0%	0%	-51
QASSIM		301	17-Feb-26 08:00	16-Dec-26 17:00	17-Feb-26 08:00 A	14-Feb-27 15:24	14,543,486.11	12,407,011.96	17,537,540.00	82.93%	70.75%	-51
MOBILIZATION		29	17-Feb-26 08:00	29-Mar-26 10:00	17-Feb-26 08:00 A	28-Mar-26 17:00 A	0.00	0.00	0.00	0%	0%	0
TEMPORARY CAMP		28	17-Feb-26 08:00	28-Mar-26 09:00	17-Feb-26 08:00 A	27-Mar-26 17:00 A	0.00	0.00	0.00	0%	0%	0
SITE OFFICES		29	17-Feb-26 08:00	29-Mar-26 10:00	17-Feb-26 08:00 A	28-Mar-26 17:00 A	0.00	0.00	0.00	0%	0%	0
GENERAL REQUIEREMENTS		57	17-Feb-26 08:00	30-Apr-26 10:00	17-Feb-26 08:00 A	29-Apr-26 17:00 A	0.00	0.00	0.00	0%	0%	0
ENGINEERING		199	17-Feb-26 08:00	16-Aug-26 17:00	17-Feb-26 08:00 A	25-Oct-26 15:24	526,126.20	526,126.20	526,126.20	100%	100%	-59
SHOP DRAWINGS SUBMITTALS		168	17-Feb-26 08:00	04-Aug-26 17:00	17-Feb-26 08:00 A	25-Oct-26 15:24	0.00	0.00	0.00	0%	0%	-69
STRUCTURAL DRAWINGS		125	17-Feb-26 08:00	06-Jul-26 17:00	17-Feb-26 08:00 A	11-Jul-26 17:00 A	0.00	0.00	0.00	0%	0%	-4
PROJECT FENCE		19	29-Apr-26 08:00	21-May-26 10:00	29-Apr-26 08:00 A	20-May-26 17:00 A	0.00	0.00	0.00	0%	0%	0
PADEL PLAYGROUND FENCE		19	29-Apr-26 08:00	21-May-26 10:00	29-Apr-26 08:00 A	20-May-26 17:00 A	0.00	0.00	0.00	0%	0%	0
AIR DOME		10	25-Jun-26 08:00	06-Jul-26 17:00	01-Jul-26 08:00 A	11-Jul-26 17:00 A	0.00	0.00	0.00	0%	0%	1
TOILET BUILDING		43	17-Feb-26 08:00	14-Apr-26 10:00	17-Feb-26 08:00 A	13-Apr-26 17:00 A	0.00	0.00	0.00	0%	0%	0
WATER STORAGE TANK		41	19-Feb-26 08:00	14-Apr-26 10:00	19-Feb-26 08:00 A	13-Apr-26 17:00 A	0.00	0.00	0.00	0%	0%	0
SEPTIC TANK		13	28-Apr-26 08:00	13-May-26 10:00	28-Apr-26 08:00 A	12-May-26 17:00 A	0.00	0.00	0.00	0%	0%	0
ARCHITECTURAL DRAWINGS		158	19-Feb-26 08:00	23-Jul-26 17:00	19-Feb-26 08:00 A	10-Sep-26 12:00 A	0.00	0.00	0.00	0%	0%	-42
TOILET BUILDING		42	19-Feb-26 08:00	15-Apr-26 10:36	19-Feb-26 08:00 A	15-Apr-26 09:36 A	0.00	0.00	0.00	0%	0%	0
AIR DOME		15	07-Jul-26 08:00	23-Jul-26 17:00	14-Aug-26 08:00 A	10-Sep-26 12:00 A	0.00	0.00	0.00	0%	0%	-9
LANDSCAPE DRAWINGS		39	23-Feb-26 08:00	14-Apr-26 10:00	23-Feb-26 08:00 A	13-Apr-26 17:00 A	0.00	0.00	0.00	0%	0%	0
MECHANICAL DRAWINGS		143	28-Feb-26 08:00	15-Jul-26 17:00	28-Feb-26 08:00 A	25-Oct-26 15:24	0.00	0.00	0.00	0%	0%	-86
WATER SUPPLY SYSTEM		32	28-Feb-26 08:00	11-Apr-26 10:00	28-Feb-26 08:00 A	09-Apr-26 17:00 A	0.00	0.00	0.00	0%	0%	0
SEWER AND DRAINAGE SYSTEM		28	04-Mar-26 08:00	11-Apr-26 10:00	04-Mar-26 08:00 A	09-Apr-26 17:00 A	0.00	0.00	0.00	0%	0%	0
IRRIGATION SYSTEM		24	09-Mar-26 08:00	11-Apr-26 10:00	09-Mar-26 08:00 A	09-Apr-26 17:00 A	0.00	0.00	0.00	0%	0%	0
AIR DOME		18	25-Jun-26 08:00	15-Jul-26 17:00	30-Jul-26 08:00 A	25-Oct-26 15:24	0.00	0.00	0.00	0%	0%	-56
ELECTRICAL DRAWINGS		102	11-May-26 08:00	04-Aug-26 17:00	11-May-26 08:00 A	25-Oct-26 14:36	0.00	0.00	0.00	0%	0%	-69
POWER AND LIGHTING SYSTEM		27	11-May-26 08:00	16-Jun-26 10:00	11-May-26 08:00 A	15-Jun-26 17:00 A	0.00	0.00	0.00	0%	0%	0
ELV SYSTEM		27	11-May-26 08:00	16-Jun-26 10:00	11-May-26 08:00 A	15-Jun-26 17:00 A	0.00	0.00	0.00	0%	0%	0
FIRE ALARM SYSTEM		27	11-May-26 08:00	16-Jun-26 10:00	11-May-26 08:00 A	15-Jun-26 17:00 A	0.00	0.00	0.00	0%	0%	0
AIR DOME		17	16-Jul-26 08:00	04-Aug-26 17:00	30-Jul-26 08:00 A	25-Oct-26 14:36	0.00	0.00	0.00	0%	0%	-57
SHOP DRAWINGS APPROVALS		172	19-Feb-26 08:00	16-Aug-26 17:00	19-Feb-26 08:00 A	21-Sep-26 08:48 A	0.00	0.00	0.00	0%	0%	-30
STRUCTURAL DRAWINGS		130	19-Feb-26 08:00	14-Jul-26 17:00	19-Feb-26 08:00 A	12-Jul-26 17:00 A	0.00	0.00	0.00	0%	0%	2
PROJECT FENCE		7	13-May-26 08:00	21-May-26 10:00	13-May-26 08:00 A	20-May-26 17:00 A	0.00	0.00	0.00	0%	0%	0
PADEL PLAYGROUND FENCE		9	11-May-26 08:00	21-May-26 10:00	11-May-26 08:00 A	20-May-26 17:00 A	0.00	0.00	0.00	0%	0%	0
AIR DOME		9	05-Jul-26 08:00	14-Jul-26 17:00	06-Jul-26 08:00 A	12-Jul-26 17:00 A	0.00	0.00	0.00	0%	0%	3
TOILET BUILDING		44	19-Feb-26 08:00	18-Apr-26 10:00	19-Feb-26 08:00 A	16-Apr-26 17:00 A	0.00	0.00	0.00	0%	0%	0
WATER STORAGE TANK		42	23-Feb-26 08:00	18-Apr-26 10:00	23-Feb-26 08:00 A	16-Apr-26 17:00 A	0.00	0.00	0.00	0%	0%	0
SEPTIC TANK		3	11-May-26 08:00	14-May-26 10:00	11-May-26 08:00 A	13-May-26 17:00 A	0.00	0.00	0.00	0%	0%	0
ARCHITECTURAL DRAWINGS		166	25-Feb-26 08:00	01-Aug-26 17:00	25-Feb-26 08:00 A	21-Sep-26 08:48 A	0.00	0.00	0.00	0%	0%	-43
TOILET BUILDING		40	25-Feb-26 08:00	18-Apr-26 10:00	25-Feb-26 08:00 A	16-Apr-26 17:00 A	0.00	0.00	0.00	0%	0%	0
AIR DOME		7	25-Jul-26 08:00	01-Aug-26 17:00	20-Aug-26 08:00 A	21-Sep-26 08:48 A	0.00	0.00	0.00	0%	0%	-20
LANDSCAPE DRAWINGS		39	26-Feb-26 08:00	18-Apr-26 10:00	26-Feb-26 08:00 A	16-Apr-26 17:00 A	0.00	0.00	0.00	0%	0%	0
MECHANICAL DRAWINGS		154	09-Mar-26 08:00	27-Jul-26 17:00	09-Mar-26 08:00 A	21-Sep-26 08:48 A	0.00	0.00	0.00	0%	0%	-47
WATER SUPPLY SYSTEM		27	09-Mar-26 08:00	14-Apr-26 10:00	09-Mar-26 08:00 A	13-Apr-26 17:00 A	0.00	0.00	0.00	0%	0%	0
SEWER AND DRAINAGE SYSTEM		27	09-Mar-26 08:00	14-Apr-26 10:00	09-Mar-26 08:00 A	13-Apr-26 17:00 A	0.00	0.00	0.00	0%	0%	0
IRRIGATION SYSTEM		24	12-Mar-26 08:00	14-Apr-26 10:00	12-Mar-26 08:00 A	13-Apr-26 17:00 A	0.00	0.00	0.00	0%	0%	0
AIR DOME		10	16-Jul-26 08:00	27-Jul-26 17:00	20-Aug-26 08:00 A	21-Sep-26 08:48 A	0.00	0.00	0.00	0%	0%	-17
ELECTRICAL DRAWINGS		100	20-May-26 08:00	16-Aug-26 17:00	20-May-26 08:00 A	21-Sep-26 08:48 A	0.00	0.00	0.00	0%	0%	-30
POWER AND LIGHTING SYSTEM		20	20-May-26 08:00	17-Jun-26 10:00	20-May-26 08:00 A	16-Jun-26 17:00 A	0.00	0.00	0.00	0%	0%	0
ELV SYSTEM		20	20-May-26 08:00	17-Jun-26 10:00	20-May-26 08:00 A	16-Jun-26 17:00 A	0.00	0.00	0.00	0%	0%	0
FIRE ALARM SYSTEM		20	20-May-26 08:00	17-Jun-26 10:00	20-May-26 08:00 A	16-Jun-26 17:00 A	0.00	0.00	0.00	0%	0%	0
AIR DOME		17	28-Jul-26 08:00	16-Aug-26 17:00	20-Aug-26 08:00 A	21-Sep-26 08:48 A	0.00	0.00	0.00	0%	0%	-10
MATERIAL SUBMITTALS		134	17-Feb-26 08:00	16-Jul-26 17:00	17-Feb-26 08:00 A	20-Aug-26 17:00 A	0.00	0.00	0.00	0%	0%	-30
LONG LEAD ITEMS		134	17-Feb-26 08:00	16-Jul-26 17:00	17-Feb-26 08:00 A	20-Aug-26 17:00 A	0.00	0.00	0.00	0%	0%	-30
EXTERNAL / LANDSCAPE WORK		56	25-Feb-26 08:00	06-May-26 10:00	25-Feb-26 08:00 A	05-May-26 17:00 A	0.00	0.00	0.00	0%	0%	0
SPORTS & RECREATIONAL FACILITIES WORK		134	17-Feb-26 08:00	16-Jul-26 17:00	17-Feb-26 08:00 A	20-Aug-26 17:00 A	0.00	0.00	0.00	0%	0%	-30
CONCRETE WORK		43	04-Mar-26 08:00	28-Apr-26 10:00	04-Mar-26 08:00 A	27-Apr-26 17:00 A	0.00	0.00	0.00	0%	0%	0
METAL WORK		47	09-Mar-26 08:00	07-May-26 10:00	09-Mar-26 08:00 A	06-May-26 17:00 A	0.00	0.00	0.00	0%	0%	0
PLUMBING WORK		46	10-Mar-26 08:00	07-May-26 10:00	10-Mar-26 08:00 A	06-May-26 17:00 A	0.00	0.00	0.00	0%	0%	0
IRRIGATION WORK		50	05-Mar-26 08:00	07-May-26 10:00	05-Mar-26 08:00 A	06-May-26 17:00 A	0.00	0.00	0.00	0%	0%	0
ELECTRICAL WORK		26	12-May-26 08:00	16-Jun-26 10:00	12-May-26 08:00 A	15-Jun-26 17:00 A	0.00	0.00	0.00	0%	0%	0
SHORT LEAD ITEMS		28	17-Feb-26 08:00	28-Mar-26 10:00	17-Feb-26 08:00 A	27-Mar-26 17:00 A	0.00	0.00	0.00	0%	0%	0
EXTERNAL / LANDSCAPE WORK		23	17-Feb-26 08:00	17-Mar-26 10:00	17-Feb-26 08:00 A	16-Mar-26 17:00 A	0.00	0.00	0.00	0%	0%	0
CONCRETE WORK		28	17-Feb-26 08:00	28-Mar-26 10:00	17-Feb-26 08:00 A	27-Mar-26 17:00 A	0.00	0.00	0.00	0%	0%	0
ARCHITECTURAL & FINISHES WORK		18	21-Feb-26 08:00	15-Mar-26 10:00	21-Feb-26 08:00 A	14-Mar-26 17:00 A	0.00	0.00	0.00	0%	0%	0
METAL WORK		11	04-Mar-26 08:00	17-Mar-26 10:00	04-Mar-26 08:00 A	16-Mar-26 17:00 A	0.00	0.00	0.00	0%	0%	0
HVAC WORK		19	23-Feb-26 08:00	17-Mar-26 10:00	23-Feb-26 08:00 A	16-Mar-26 17:00 A	0.00	0.00	0.00	0%	0%	0
PLUMBING WORK		4	12-Mar-26 08:00	17-Mar-26 10:00	12-Mar-26 08:00 A	16-Mar-26 17:00 A	0.00	0.00	0.00	0%	0%	0
IRRIGATION WORK		17	25-Feb-26 08:00	17-Mar-26 10:00	25-Feb-26 08:00 A	16-Mar-26 17:00 A	0.00	0.00	0.00	0%	0%	0

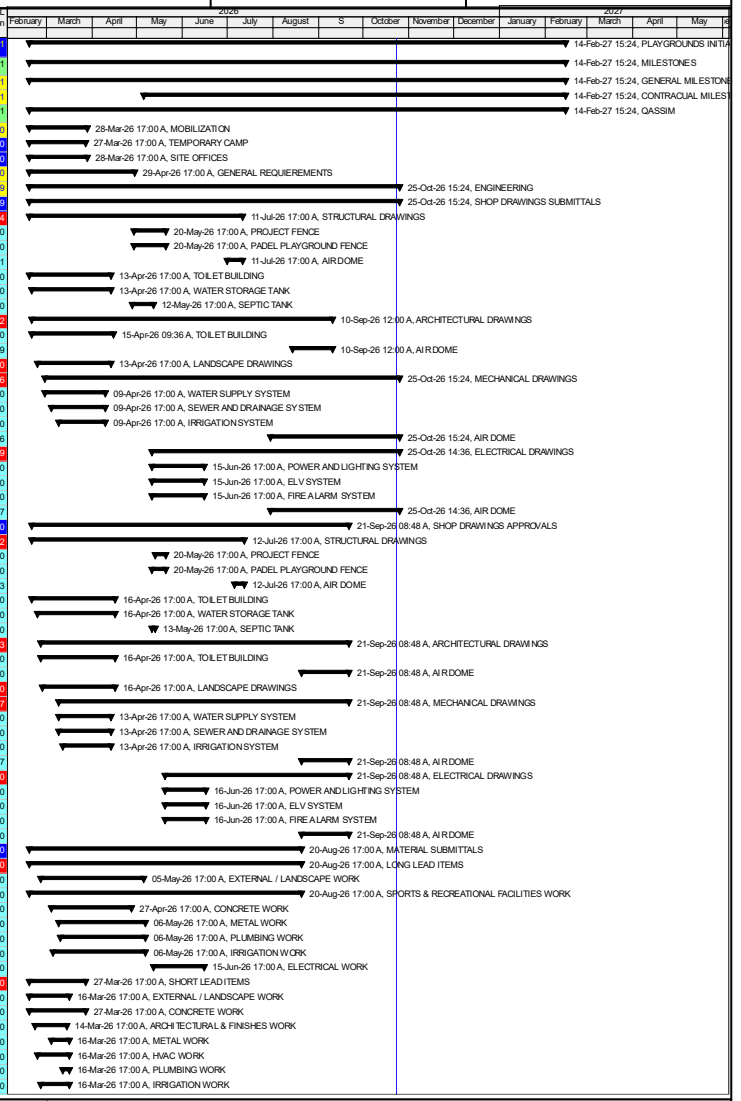

Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining W...
Milestone
summary

Baseline Schedule Rev.00


PLAYGROUNDS INITIATIVE - QASSIM, HAIL & TABUK - 25-Oct-2026

شركة الإنشاء المتقدم للمقاولات
Advanced Construction For Cont. Co

egis

مدن

Activity ID	Activity Name	O.D	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Schedule % Complete	Performance % Complete	Variance - BL Project Duration
	ELECTRICAL WORK	4	12-Mar-26 08:00	17-Mar-26 10:00	12-Mar-26 08:00 A	16-Mar-26 17:00 A	0.00	0.00	0.00	0%	0%	0
	FIRE FIGHTING WORK	4	12-Mar-26 08:00	17-Mar-26 10:00	12-Mar-26 08:00 A	16-Mar-26 17:00 A	0.00	0.00	0.00	0%	0%	0
	MATERIAL APPROVALS	196	21-Feb-26 08:00	18-Jul-26 17:00	21-Feb-26 08:00 A	01-Oct-26 17:00 A	526,126.20	526,126.20	526,126.20	100%	100%	-64
	LONG LEAD ITEMS	189	02-Mar-26 08:00	18-Jul-26 17:00	02-Mar-26 08:00 A	01-Oct-26 17:00 A	358,885.26	358,885.26	358,885.26	100%	100%	-64
	EXTERNAL / LANDSCAPE WORK	2	11-May-26 08:00	12-May-26 17:00	11-May-26 08:00 A	12-May-26 17:00 A	19,812.18	19,812.18	19,812.18	100%	100%	0
	SPORTS & RECREATIONAL FACILITIES WORK	110	02-Mar-26 08:00	30-Jun-26 17:00	02-Mar-26 08:00 A	19-Sep-26 12:00 A	273,522.54	273,522.54	273,522.54	100%	100%	-69
	CONCRETE WORK	40	09-Mar-26 08:00	28-Apr-26 17:00	09-Mar-26 08:00 A	28-Apr-26 17:00 A	1,417.50	1,417.50	1,417.50	100%	100%	0
	METAL WORK	112	09-Jun-26 08:00	18-Jul-26 17:00	09-Jun-26 08:00 A	01-Oct-26 17:00 A	889.23	889.23	889.23	100%	100%	-64
	PLUMBING WORK	48	09-Jun-26 08:00	18-Jul-26 17:00	20-May-26 08:00 A	24-Jun-26 17:00 A	3,553.95	3,553.95	3,553.95	100%	100%	7
	IRRIGATION WORK	45	11-Mar-26 08:00	06-May-26 17:00	11-Mar-26 08:00 A	06-May-26 17:00 A	24,486.75	24,486.75	24,486.75	100%	100%	0
	ELECTRICAL WORK	96	12-May-26 08:00	02-Jul-26 17:00	12-May-26 08:00 A	16-Sep-26 08:24 A	35,203.11	35,203.11	35,203.11	100%	100%	-64
	SHORT LEAD ITEMS	25	21-Feb-26 08:00	26-Mar-26 17:00	21-Feb-26 08:00 A	26-Mar-26 17:00 A	167,240.94	167,240.94	167,240.94	100%	100%	0
	EXTERNAL / LANDSCAPE WORK	25	21-Feb-26 08:00	26-Mar-26 17:00	21-Feb-26 08:00 A	26-Mar-26 17:00 A	139,867.29	139,867.29	139,867.29	100%	100%	0
	CONCRETE WORK	24	23-Feb-26 08:00	26-Mar-26 17:00	23-Feb-26 08:00 A	26-Mar-26 17:00 A	1,609.47	1,609.47	1,609.47	100%	100%	0
	ARCHITECTURAL & FINISHES WORK	17	25-Feb-26 08:00	16-Mar-26 17:00	25-Feb-26 08:00 A	16-Mar-26 17:00 A	7,931.55	7,931.55	7,931.55	100%	100%	0
	METAL WORK	12	09-Mar-26 08:00	26-Mar-26 17:00	09-Mar-26 08:00 A	26-Mar-26 17:00 A	478.89	478.89	478.89	100%	100%	0
	HVAC WORK	20	28-Feb-26 08:00	26-Mar-26 17:00	28-Feb-26 08:00 A	26-Mar-26 17:00 A	606.36	606.36	606.36	100%	100%	0
	PLUMBING WORK	2	25-Mar-26 08:00	26-Mar-26 17:00	25-Mar-26 08:00 A	26-Mar-26 17:00 A	3,147.03	3,147.03	3,147.03	100%	100%	0
	IRRIGATION WORK	17	03-Mar-26 08:00	26-Mar-26 17:00	03-Mar-26 08:00 A	26-Mar-26 17:00 A	13,170.12	13,170.12	13,170.12	100%	100%	0
	ELECTRICAL WORK	2	25-Mar-26 08:00	26-Mar-26 17:00	25-Mar-26 08:00 A	26-Mar-26 17:00 A	407.52	407.52	407.52	100%	100%	0
	FIRE FIGHTING WORK	2	25-Mar-26 08:00	26-Mar-26 17:00	25-Mar-26 08:00 A	26-Mar-26 17:00 A	22.71	22.71	22.71	100%	100%	0
	PROCUREMENT	226	03-Mar-26 08:00	27-Aug-26 17:00	03-Mar-26 08:00 A	28-Oct-26 12:00	4,735,135.80	4,306,400.85	4,735,135.80	100%	90.95%	-52
	LONG LEAD ITEMS	213	18-Mar-26 08:00	27-Aug-26 17:00	18-Mar-26 08:00 A	28-Oct-26 12:00	3,229,967.34	2,816,604.28	3,229,967.34	100%	87.2%	-52
	PURCHASE ORDER	147	18-Mar-26 08:00	12-Jul-26 17:00	18-Mar-26 08:00 A	16-Sep-26 12:48 A	0.00	0.00	0.00	0%	0%	-57
	EXTERNAL / LANDSCAPE WORK	5	06-May-26 08:00	12-May-26 10:00	06-May-26 08:00 A	11-May-26 17:00 A	0.00	0.00	0.00	0%	0%	0
	SPORTS & RECREATIONAL FACILITIES WORK	101	26-Mar-26 08:00	09-Jul-26 17:00	26-Mar-26 08:00 A	09-Jul-26 17:00 A	0.00	0.00	0.00	0%	0%	0
	CONCRETE WORK	39	18-Mar-26 08:00	07-May-26 10:00	18-Mar-26 08:00 A	06-May-26 17:00 A	0.00	0.00	0.00	0%	0%	0
	METAL WORK	36	26-Mar-26 08:00	07-May-26 10:00	26-Mar-26 08:00 A	06-May-26 17:00 A	0.00	0.00	0.00	0%	0%	0
	PLUMBING WORK	34	29-Mar-26 08:00	07-May-26 10:00	29-Mar-26 08:00 A	06-May-26 17:00 A	0.00	0.00	0.00	0%	0%	0
	IRRIGATION WORK	37	25-Mar-26 08:00	07-May-26 10:00	25-Mar-26 08:00 A	06-May-26 17:00 A	0.00	0.00	0.00	0%	0%	0
	ELECTRICAL WORK	103	13-May-26 08:00	12-Jul-26 17:00	13-May-26 08:00 A	16-Sep-26 12:48 A	0.00	0.00	0.00	0%	0%	-57
	MANUFACTURE / FABRICATION	161	05-May-26 08:00	11-Aug-26 17:00	05-May-26 08:00 A	04-Oct-26 17:00 A	0.00	0.00	0.00	0%	0%	-45
	EXTERNAL / LANDSCAPE WORK	109	05-May-26 08:00	23-Jul-26 17:00	05-May-26 08:00 A	16-Sep-26 12:00 A	0.00	0.00	0.00	0%	0%	-47
	SPORTS & RECREATIONAL FACILITIES WORK	123	05-May-26 08:00	11-Aug-26 17:00	05-May-26 08:00 A	16-Sep-26 12:00 A	0.00	0.00	0.00	0%	0%	-31
	CONCRETE WORK	69	05-May-26 08:00	12-Jul-26 17:00	05-May-26 08:00 A	24-Jun-26 17:00 A	0.00	0.00	0.00	0%	0%	15
	METAL WORK	161	05-May-26 08:00	23-Jul-26 17:00	05-May-26 08:00 A	04-Oct-26 17:00 A	0.00	0.00	0.00	0%	0%	-61
	PLUMBING WORK	79	05-May-26 08:00	23-Jul-26 17:00	05-May-26 08:00 A	24-Jun-26 17:00 A	0.00	0.00	0.00	0%	0%	25
	IRRIGATION WORK	82	05-May-26 08:00	06-Jul-26 17:00	05-May-26 08:00 A	16-Sep-26 12:00 A	0.00	0.00	0.00	0%	0%	-62
	ELECTRICAL WORK	129	12-May-26 08:00	10-Aug-26 17:00	12-May-26 08:00 A	16-Sep-26 12:00 A	0.00	0.00	0.00	0%	0%	-32
	DELIVERY TO SITE	175	06-May-26 08:00	27-Aug-26 17:00	06-May-26 08:00 A	28-Oct-26 12:00	3,229,967.34	2,816,604.28	3,229,967.34	100%	87.2%	-52
	EXTERNAL / LANDSCAPE WORK	123	06-May-26 08:00	10-Aug-26 17:00	06-May-26 08:00 A	25-Oct-26 12:00	178,309.62	176,866.75	178,309.62	100%	99.19%	-64
	SPORTS & RECREATIONAL FACILITIES WORK	127	06-May-26 08:00	23-Aug-26 17:00	06-May-26 08:00 A	27-Oct-26 15:24	2,461,702.86	2,073,940.31	2,461,702.86	100%	84.25%	-55
	CONCRETE WORK	78	06-May-26 08:00	23-Jul-26 17:00	06-May-26 08:00 A	05-Jul-26 17:00 A	12,757.50	12,757.50	12,757.50	100%	100%	16
	METAL WORK	175	06-May-26 08:00	10-Aug-26 17:00	06-May-26 08:00 A	28-Oct-26 12:00	8,003.07	6,974.78	8,003.07	100%	87.15%	-67
	PLUMBING WORK	104	06-May-26 08:00	10-Aug-26 17:00	06-May-26 08:00 A	13-Oct-26 17:00 A	31,985.55	31,985.55	31,985.55	100%	100%	-54
	IRRIGATION WORK	102	06-May-26 08:00	15-Jul-26 17:00	06-May-26 08:00 A	24-Oct-26 11:12	220,380.75	219,357.96	220,380.75	100%	99.54%	-84
	ELECTRICAL WORK	143	13-May-26 08:00	27-Aug-26 17:00	13-May-26 08:00 A	25-Oct-26 12:00	316,827.99	294,721.44	316,827.99	100%	93.02%	-49
	SHORT LEAD ITEMS	183	03-Mar-26 08:00	12-Jul-26 17:00	03-Mar-26 08:00 A	25-Oct-26 12:00	1,505,168.46	1,489,796.57	1,505,168.46	100%	98.98%	-89
	PURCHASE ORDER	64	03-Mar-26 08:00	21-May-26 10:00	03-Mar-26 08:00 A	20-May-26 17:00 A	0.00	0.00	0.00	0%	0%	0
	EXTERNAL / LANDSCAPE WORK	57	03-Mar-26 08:00	13-May-26 10:00	03-Mar-26 08:00 A	12-May-26 17:00 A	0.00	0.00	0.00	0%	0%	0
	CONCRETE WORK	39	04-Mar-26 08:00	23-Apr-26 10:00	04-Mar-26 08:00 A	22-Apr-26 17:00 A	0.00	0.00	0.00	0%	0%	0
	ARCHITECTURAL & FINISHES WORK	48	07-Mar-26 08:00	06-May-26 10:00	07-Mar-26 08:00 A	05-May-26 17:00 A	0.00	0.00	0.00	0%	0%	0
	METAL WORK	36	25-Mar-26 08:00	06-May-26 10:00	25-Mar-26 08:00 A	05-May-26 17:00 A	0.00	0.00	0.00	0%	0%	0
	HVAC WORK	46	09-Mar-26 08:00	06-May-26 10:00	09-Mar-26 08:00 A	05-May-26 17:00 A	0.00	0.00	0.00	0%	0%	0
	PLUMBING WORK	33	29-Mar-26 08:00	06-May-26 10:00	29-Mar-26 08:00 A	05-May-26 17:00 A	0.00	0.00	0.00	0%	0%	0
	IRRIGATION WORK	43	12-Mar-26 08:00	06-May-26 10:00	12-Mar-26 08:00 A	05-May-26 17:00 A	0.00	0.00	0.00	0%	0%	0
	ELECTRICAL WORK	8	12-May-26 08:00	21-May-26 10:00	12-May-26 08:00 A	20-May-26 17:00 A	0.00	0.00	0.00	0%	0%	0
	FIRE FIGHTING WORK	30	01-Apr-26 08:00	06-May-26 10:00	01-Apr-26 08:00 A	05-May-26 17:00 A	0.00	0.00	0.00	0%	0%	0
	DELIVERY TO SITE	181	05-Mar-26 08:00	12-Jul-26 17:00	05-Mar-26 08:00 A	25-Oct-26 12:00	1,505,168.46	1,489,796.57	1,505,168.46	100%	98.98%	-89
	EXTERNAL / LANDSCAPE WORK	155	05-Mar-26 08:00	08-Jul-26 17:00	05-Mar-26 08:00 A	25-Oct-26 09:36	1,258,805.61	1,250,950.31	1,258,805.61	100%	99.38%	-91
	CONCRETE WORK	50	12-Mar-26 08:00	13-May-26 17:00	12-Mar-26 08:00 A	13-May-26 17:00 A	14,485.23	14,485.23	14,485.23	100%	100%	0
	ARCHITECTURAL & FINISHES WORK	7	06-May-26 08:00	13-May-26 17:00	06-May-26 08:00 A	13-May-26 17:00 A	71,383.95	71,383.95	71,383.95	100%	100%	0
	METAL WORK	129	06-May-26 08:00	08-Jul-26 17:00	06-May-26 08:00 A	25-Oct-26 09:36	4,310.01	4,137.61	4,310.01	100%	96%	-91
	HVAC WORK	106	06-May-26 08:00	08-Jul-26 17:00	06-May-26 08:00 A	02-Oct-26 09:36 A	5,457.24	5,457.24	5,457.24	100%	100%	-72
	PLUMBING WORK	7	06-May-26 08:00	13-May-26 17:00	06-May-26 08:00 A	13-May-26 17:00 A	28,323.27	28,323.27	28,323.27	100%	100%	0
	IRRIGATION WORK	101	06-May-26 08:00	08-Jul-26 17:00	06-May-26 08:00 A	25-Oct-26 09:36	118,531.08	111,419.22	118,531.08	100%	94%	-91
	ELECTRICAL WORK	128	11-May-26 08:00	12-Jul-26 17:00	11-May-26 08:00 A	25-Oct-26 12:00	3,667.68	3,447.62	3,667.68	100%	94%	-89
	FIRE FIGHTING WORK	129	06-May-26 08:00	08-Jul-26 17:00	06-May-26 08:00 A	25-Oct-26 09:36	204.39	192.13	204.39	100%	94%	-91
	CONSTRUCTION STAGE	259	24-Mar-26 08:00	16-Dec-26 17:00	24-Mar-26 08:00 A	25-Jan-27 15:24	9,229,611.49	7,250,040.43	10,522,524.00	87.71%	68.9%	-34
	PLAYGROUND AND LANDSCAPING WORKS	246	24-Mar-26 08:00	16-Dec-26 17:00	24-Mar-26 08:00 A	03-Jan-27 17:00	5,507,994.11	5,480,031.42	6,019,638.42	91.5%	91.04%	-15
	CUT AND FILL	38	24-Mar-26 08:00	06-May-26 17:00	24-Mar-26 08:00 A	06-May-26 17:00 A	900,600.00	900,600.00	900,600.00	100%	100%	0

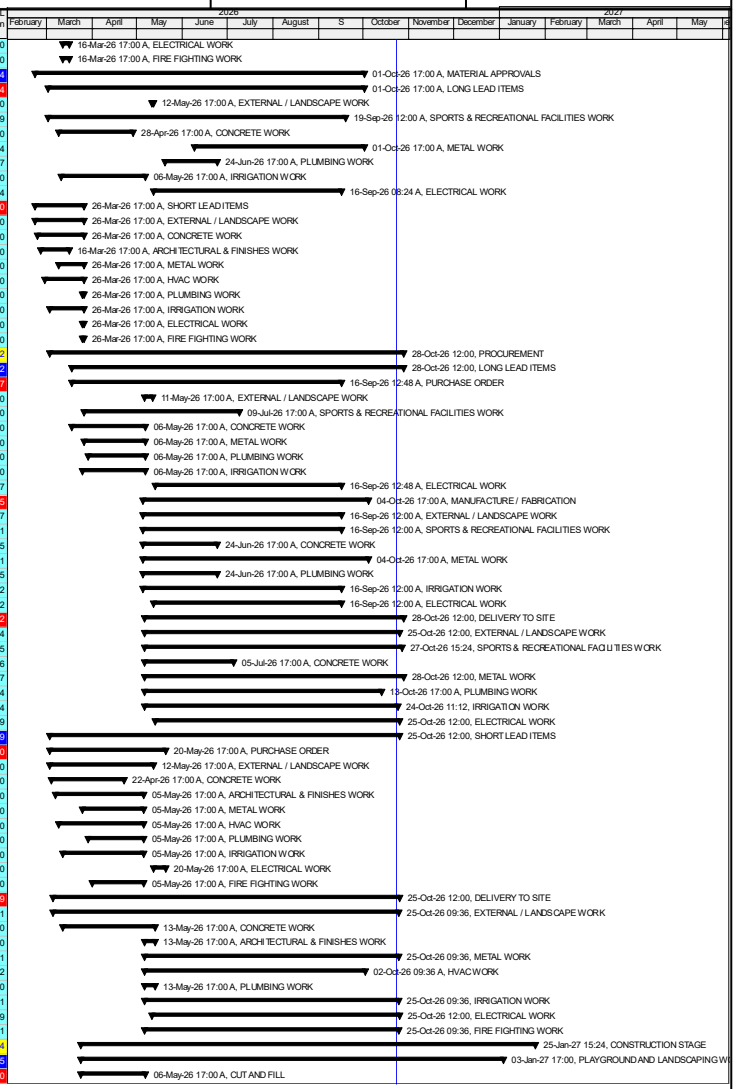


Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining W...
Milestone
summary

Baseline Schedule Rev.00

PLAYGROUNDS INITIATIVE - QASSIM, HAIL & TABUK - 25-Oct-2026

Advanced Construction For Cont. Co

Activity ID	Activity Name	O.D	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Schedule % Complete	Performance % Complete	Variance - BL Project Duration
	PLAYGROUND WORKS	198	21-Apr-26 08:00	02-Dec-26 17:00	21-Apr-26 08:00 A	14-Dec-26 10:48	1,219,061.19	1,225,919.75	1,318,471.20	92.46%	92.98%	-9
	FOOTBALL PLAYGROUND WORKS	172	21-Apr-26 08:00	17-Nov-26 17:00	21-Apr-26 08:00 A	12-Nov-26 12:48	585,918.56	572,933.63	611,282.16	95.85%	93.73%	4
	BASKETBALL PLAYGROUND WORKS	163	30-Apr-26 08:00	17-Nov-26 17:00	30-Apr-26 08:00 A	09-Nov-26 09:12	377,079.59	373,064.98	381,705.12	98.79%	97.74%	8
	PADEL PLAYGROUND WORKS	185	06-May-26 08:00	02-Dec-26 17:00	06-May-26 08:00 A	14-Dec-26 10:48	256,063.05	279,921.14	325,483.92	78.67%	86%	-9
	GENERAL SITE WORKS	226	16-Apr-26 08:00	16-Dec-26 17:00	16-Apr-26 08:00 A	03-Jan-27 17:00	1,526,282.82	1,415,562.43	1,617,941.82	94.33%	87.49%	-15
	FENCE WORKS	168	16-Apr-26 08:00	13-Sep-26 17:00	16-Apr-26 08:00 A	20-Oct-26 17:00 A	32,909.40	32,909.40	32,909.40	100%	100%	-31
	MECHANICAL WORK	159	12-May-26 08:00	18-Aug-26 17:00	12-May-26 08:00 A	19-Nov-26 11:12	780,707.34	707,170.08	780,707.34	100%	90.58%	-78
	STORM WATER AND UTILITY WORK	157	12-May-26 08:00	16-Aug-26 17:00	12-May-26 08:00 A	17-Nov-26 11:12	27,252.00	19,573.20	27,252.00	100%	71.82%	-78
	IRRIGATION SYSTEM WORKS	86	17-Jun-26 08:00	09-Aug-26 17:00	17-Jun-26 08:00 A	10-Nov-26 11:12	753,137.40	687,596.88	753,137.40	100%	91.3%	-78
	FIRE PROTECTION SYSTEM	2	17-Aug-26 08:00	18-Aug-26 17:00	17-Nov-26 11:12	19-Nov-26 11:12	317.94	0.00	317.94	100%	0%	0
	ELECTRICAL WORK	197	20-May-26 08:00	01-Nov-26 17:00	20-May-26 08:00 A	14-Dec-26 09:36	692,767.08	582,802.15	693,965.28	99.83%	83.98%	-36
	POWER, LIGHTING & GROUNDING	162	20-May-26 08:00	20-Sep-26 17:00	20-May-26 08:00 A	28-Nov-26 09:36	636,895.08	548,560.03	636,895.08	100%	86.13%	-57
	ELV SYSTEMS (TELECOM, DATA, AV & CCTV)	25	21-Sep-26 08:00	20-Oct-26 17:00	07-Oct-26 08:00 A	09-Dec-26 09:36	43,146.00	25,887.60	43,146.00	100%	60%	-29
	FIRE ALARM SYSTEM	32	26-Sep-26 08:00	01-Nov-26 17:00	11-Oct-26 08:00 A	14-Dec-26 09:36	12,726.00	8,354.52	13,924.20	91.39%	60%	-23
	PARKING WORK	157	17-Jun-26 08:00	09-Nov-26 17:00	17-Jun-26 08:00 A	15-Dec-26 09:36	19,899.00	88,440.00	102,919.80	19.33%	85.93%	-30
	SERVICE CONNECTION	38	10-Nov-26 08:00	16-Dec-26 17:00	12-Jul-26 08:00 A	03-Jan-27 17:00	0.00	4,240.80	7,440.00	0%	57%	-118
	LANDSCAPING WORKS	168	31-May-26 08:00	14-Dec-26 17:00	30-May-26 08:48 A	26-Nov-26 14:36	1,813,759.70	1,900,072.74	2,134,335.00	84.98%	89.02%	15
	HARDSCAPE WORK	168	31-May-26 08:00	14-Dec-26 17:00	30-May-26 08:48 A	26-Nov-26 14:36	1,644,359.70	1,692,172.74	1,712,409.00	96.03%	98.82%	15
	SOFTSCAPE WORK	139	10-Jun-26 08:00	21-Nov-26 17:00	10-Jun-26 08:00 A	19-Nov-26 14:36	169,400.00	207,900.00	421,926.00	40.15%	49.27%	1
	TANK WORKS	138	13-May-26 08:00	19-Aug-26 17:00	13-May-26 08:00 A	26-Oct-26 11:12	48,290.40	37,876.50	48,290.40	100%	78.43%	-56
	SEPTIC TANK	33	13-May-26 08:00	24-Jun-26 17:00	13-May-26 08:00 A	24-Jun-26 17:00 A	7,475.22	7,475.22	7,475.22	100%	100%	0
	WATER STORAGE TANK	138	13-May-26 08:00	19-Aug-26 17:00	13-May-26 08:00 A	26-Oct-26 11:12	40,815.18	30,401.28	40,815.18	100%	74.49%	-56
	AIR DOME CONSTRUCTION	216	13-May-26 08:00	26-Nov-26 17:00	13-May-26 08:00 A	25-Jan-27 15:24	3,396,773.00	1,461,181.68	4,178,041.20	81.3%	34.97%	-51
	CIVIL WORK	155	13-May-26 08:00	10-Sep-26 17:00	13-May-26 08:00 A	15-Nov-26 15:24	1,711,669.97	1,210,693.39	1,711,669.97	100%	70.73%	-55
	ARCHITECTURAL WORK	45	27-Oct-26 08:00	26-Nov-26 17:00	27-Aug-26 08:00 A	25-Jan-27 15:24	0.00	125,244.14	712,953.22	0%	17.57%	-102
	MECHANICAL WORK	16	12-Sep-26 08:00	30-Sep-26 17:00	15-Nov-26 15:24	03-Dec-26 15:24	667,968.77	0.00	667,968.77	100%	0%	0
	ELECTRICAL WORK	90	17-Aug-26 08:00	26-Oct-26 17:00	27-Aug-26 08:00 A	29-Dec-26 15:24	1,017,134.26	125,244.14	1,085,449.25	93.71%	11.54%	-46
	TOILET BUILDING WORKS	163	06-May-26 08:00	20-Oct-26 17:00	06-May-26 08:00 A	31-Oct-26 10:24	324,844.38	308,827.33	324,844.38	100%	95.07%	-8
	CIVIL WORK	162	06-May-26 08:00	19-Oct-26 17:00	06-May-26 08:00 A	29-Oct-26 17:00	227,117.58	214,414.56	227,117.58	100%	94.41%	-9
	STRUCTURAL WORK	85	06-May-26 08:00	04-Aug-26 17:00	06-May-26 08:00 A	10-Jul-26 17:00 A	37,980.00	37,980.00	37,980.00	100%	100%	22
	ARCHITECTURAL WORK	107	05-Aug-26 08:00	19-Oct-26 17:00	12-Jul-26 08:00 A	29-Oct-26 17:00	189,137.58	176,434.56	189,137.58	100%	93.28%	-30
	GENERAL FINISHES	107	05-Aug-26 08:00	19-Oct-26 17:00	12-Jul-26 08:00 A	29-Oct-26 17:00	84,120.00	77,872.38	84,120.00	100%	92.57%	-30
	WET AREA FINISHES	59	20-Aug-26 08:00	14-Oct-26 17:00	06-Aug-26 08:00 A	27-Oct-26 12:48	81,123.78	79,515.30	81,123.78	100%	98.02%	-23
	ROOF FINISHES	14	01-Oct-26 08:00	19-Oct-26 17:00	20-Aug-26 08:00 A	29-Oct-26 17:00	23,893.80	19,046.88	23,893.80	100%	79.71%	-44
	MEP WORK	132	16-Jun-26 08:00	20-Oct-26 17:00	16-Jun-26 08:00 A	31-Oct-26 10:24	97,726.80	94,412.77	97,726.80	100%	96.61%	-8
	MECANICAL WORKS	132	16-Jun-26 08:00	20-Oct-26 17:00	16-Jun-26 08:00 A	31-Oct-26 10:24	79,479.48	76,165.45	79,479.48	100%	95.83%	-8
	FIRE FIGHTING SYSTEM	1	20-Oct-26 08:00	20-Oct-26 17:00	01-Oct-26 08:00 A	31-Oct-26 10:24	136.26	95.38	136.26	100%	70%	-24
	SEWER AND DRAINAGE SYSTEM	103	16-Jun-26 08:00	02-Sep-26 17:00	16-Jun-26 08:00 A	26-Oct-26 08:48	11,290.02	10,322.30	11,290.02	100%	91.43%	-44
	HVAC SYSTEM	26	12-Aug-26 08:00	23-Aug-26 17:00	13-Aug-26 08:00 A	24-Oct-26 16:12	12,127.20	9,821.76	12,127.20	100%	80.99%	-51
	WATER SUPPLY SYSTEM	80	16-Jun-26 08:00	31-Aug-26 17:00	16-Jun-26 08:00 A	07-Sep-26 10:24 A	55,926.00	55,926.00	55,926.00	100%	100%	-5
	ELECTRICAL WORKS	47	13-Jul-26 08:00	15-Sep-26 17:00	22-Jul-26 08:00 A	08-Sep-26 15:24 A	18,247.32	18,247.32	18,247.32	100%	100%	14
	PROJECT CLOSOUT	225	23-May-26 08:00	16-Dec-26 17:00	22-May-26 09:36 A	14-Feb-27 15:24	52,612.62	324,444.49	1,753,754.00	3%	18.5%	-51
	HAIL	272	17-Feb-26 08:00	15-Dec-26 17:00	17-Feb-26 08:00 A	09-Jan-27 12:48	6,006,753.31	5,675,326.67	6,814,652.00	88.14%	83.28%	-21
	MOBILIZATION	29	17-Feb-26 08:00	29-Mar-26 10:00	17-Feb-26 08:00 A	28-Mar-26 17:00 A	0.00	0.00	0.00	0%	0%	0
	TEMPORARY CAMP	28	17-Feb-26 08:00	28-Mar-26 09:00	17-Feb-26 08:00 A	27-Mar-26 17:00 A	0.00	0.00	0.00	0%	0%	0
	SITE OFFICES	29	17-Feb-26 08:00	29-Mar-26 10:00	17-Feb-26 08:00 A	28-Mar-26 17:00 A	0.00	0.00	0.00	0%	0%	0
	GENERAL REQUIEREMENTS	51	17-Feb-26 08:00	23-Apr-26 10:00	17-Feb-26 08:00 A	22-Apr-26 17:00 A	0.00	0.00	0.00	0%	0%	0
	ENGINEERING	168	17-Feb-26 08:00	14-Jul-26 17:00	17-Feb-26 08:00 A	17-Sep-26 17:00 A	204,439.56	204,439.56	204,439.56	100%	100%	-56
	SHOP DRAWINGS SUBMITTALS	93	17-Feb-26 08:00	16-Jun-26 10:00	17-Feb-26 08:00 A	15-Jun-26 17:00 A	0.00	0.00	0.00	0%	0%	0
	STRUCTURAL DRAWINGS	61	17-Feb-26 08:00	05-May-26 10:00	17-Feb-26 08:00 A	04-May-26 17:00 A	0.00	0.00	0.00	0%	0%	0
	PROJECT FENCE	57	17-Feb-26 08:00	30-Apr-26 10:00	17-Feb-26 08:00 A	29-Apr-26 17:00 A	0.00	0.00	0.00	0%	0%	0
	TOILET BUILDING	41	19-Feb-26 08:00	14-Apr-26 10:00	19-Feb-26 08:00 A	13-Apr-26 17:00 A	0.00	0.00	0.00	0%	0%	0
	WATER STORAGE TANK	39	23-Feb-26 08:00	14-Apr-26 10:00	23-Feb-26 08:00 A	13-Apr-26 17:00 A	0.00	0.00	0.00	0%	0%	0
	SEPTIC TANK	55	25-Feb-26 08:00	05-May-26 10:00	25-Feb-26 08:00 A	04-May-26 17:00 A	0.00	0.00	0.00	0%	0%	0
	ARCHITECTURAL DRAWINGS	39	23-Feb-26 08:00	14-Apr-26 10:00	23-Feb-26 08:00 A	13-Apr-26 17:00 A	0.00	0.00	0.00	0%	0%	0
	TOILET BUILDING	39	23-Feb-26 08:00	14-Apr-26 10:00	23-Feb-26 08:00 A	13-Apr-26 17:00 A	0.00	0.00	0.00	0%	0%	0
	LANDSCAPE DRAWINGS	38	24-Feb-26 08:00	14-Apr-26 10:00	24-Feb-26 08:00 A	13-Apr-26 17:00 A	0.00	0.00	0.00	0%	0%	0
	MECHANICAL DRAWINGS	52	01-Mar-26 08:00	05-May-26 10:00	01-Mar-26 08:00 A	04-May-26 17:00 A	0.00	0.00	0.00	0%	0%	0
	WATER SUPPLY SYSTEM	31	01-Mar-26 08:00	11-Apr-26 10:00	01-Mar-26 08:00 A	09-Apr-26 17:00 A	0.00	0.00	0.00	0%	0%	0
	SEWER AND DRAINAGE SYSTEM	27	05-Mar-26 08:00	11-Apr-26 10:00	05-Mar-26 08:00 A	09-Apr-26 17:00 A	0.00	0.00	0.00	0%	0%	0
	IRRIGATION SYSTEM	44	10-Mar-26 08:00	05-May-26 10:00	10-Mar-26 08:00 A	04-May-26 17:00 A	0.00	0.00	0.00	0%	0%	0
	ELECTRICAL DRAWINGS	27	11-May-26 08:00	16-Jun-26 10:00	11-May-26 08:00 A	15-Jun-26 17:00 A	0.00	0.00	0.00	0%	0%	0
	POWER AND LIGHTING SYSTEM	27	11-May-26 08:00	16-Jun-26 10:00	11-May-26 08:00 A	15-Jun-26 17:00 A	0.00	0.00	0.00	0%	0%	0
	ELV SYSTEM	27	11-May-26 08:00	16-Jun-26 10:00	11-May-26 08:00 A	15-Jun-26 17:00 A	0.00	0.00	0.00	0%	0%	0
	FIRE ALARM SYSTEM	27	11-May-26 08:00	16-Jun-26 10:00	11-May-26 08:00 A	15-Jun-26 17:00 A	0.00	0.00	0.00	0%	0%	0
	SHOP DRAWINGS APPROVALS	92	19-Feb-26 08:00	17-Jun-26 10:00	19-Feb-26 08:00 A	16-Jun-26 17:00 A	0.00	0.00	0.00	0%	0%	0
	STRUCTURAL DRAWINGS	61	19-Feb-26 08:00	07-May-26 10:00	19-Feb-26 08:00 A	06-May-26 17:00 A	0.00	0.00	0.00	0%	0%	0
	PROJECT FENCE	55	19-Feb-26 08:00	30-Apr-26 10:00	19-Feb-26 08:00 A	29-Apr-26 17:00 A	0.00	0.00	0.00	0%	0%	0
	TOILET BUILDING	42	23-Feb-26 08:00	18-Apr-26 10:00	23-Feb-26 08:00 A	16-Apr-26 17:00 A	0.00	0.00	0.00	0%	0%	0
	WATER STORAGE TANK	40	25-Feb-26 08:00	18-Apr-26 10:00	25-Feb-26 08:00 A	16-Apr-26 17:00 A	0.00	0.00	0.00	0%	0%	0
	SEPTIC TANK	54	01-Mar-26 08:00	07-May-26 10:00	01-Mar-26 08:00 A	06-May-26 17:00 A	0.00	0.00	0.00	0%	0%	0

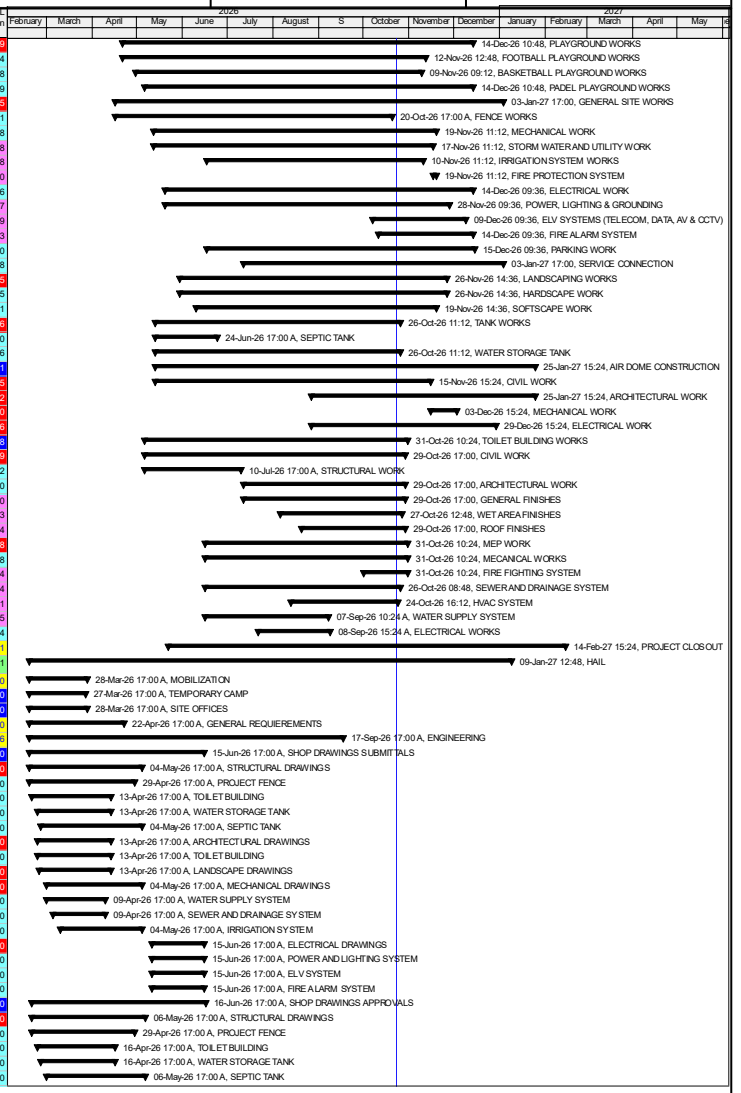


Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining W...
Milestone
summary

Baseline Schedule Rev.00

PLAYGROUNDS INITIATIVE - QASSIM, HAIL & TABUK - 25-Oct-2026

Advanced Construction For Cont. Co

Activity ID	Activity Name	O.D	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Schedule % Complete	Performance % Complete	Variance - BL Project Duration
	ARCHITECTURAL DRAWINGS	38	28-Feb-26 08:00	18-Apr-26 10:00	28-Feb-26 08:00 A	16-Apr-26 17:00 A	0.00	0.00	0.00	0%	0%	0
	TOILET BUILDING	38	28-Feb-26 08:00	18-Apr-26 10:00	28-Feb-26 08:00 A	16-Apr-26 17:00 A	0.00	0.00	0.00	0%	0%	0
	LANDSCAPE DRAWINGS	38	28-Feb-26 08:00	18-Apr-26 10:00	28-Feb-26 08:00 A	16-Apr-26 17:00 A	0.00	0.00	0.00	0%	0%	0
	MECHANICAL DRAWINGS	46	10-Mar-26 08:00	07-May-26 10:00	10-Mar-26 08:00 A	06-May-26 17:00 A	0.00	0.00	0.00	0%	0%	0
	WATER SUPPLY SYSTEM	26	10-Mar-26 08:00	14-Apr-26 10:00	10-Mar-26 08:00 A	13-Apr-26 17:00 A	0.00	0.00	0.00	0%	0%	0
	SEWER AND DRAINAGE SYSTEM	26	10-Mar-26 08:00	14-Apr-26 10:00	10-Mar-26 08:00 A	13-Apr-26 17:00 A	0.00	0.00	0.00	0%	0%	0
	IRRIGATION SYSTEM	43	14-Mar-26 08:00	07-May-26 10:00	14-Mar-26 08:00 A	06-May-26 17:00 A	0.00	0.00	0.00	0%	0%	0
	ELECTRICAL DRAWINGS	27	12-May-26 08:00	17-Jun-26 10:00	12-May-26 08:00 A	16-Jun-26 17:00 A	0.00	0.00	0.00	0%	0%	0
	POWER AND LIGHTING SYSTEM	27	12-May-26 08:00	17-Jun-26 10:00	12-May-26 08:00 A	16-Jun-26 17:00 A	0.00	0.00	0.00	0%	0%	0
	ELV SYSTEM	27	12-May-26 08:00	17-Jun-26 10:00	12-May-26 08:00 A	16-Jun-26 17:00 A	0.00	0.00	0.00	0%	0%	0
	FIRE ALARM SYSTEM	27	12-May-26 08:00	17-Jun-26 10:00	12-May-26 08:00 A	16-Jun-26 17:00 A	0.00	0.00	0.00	0%	0%	0
	MATERIAL SUBMITTALS	166	17-Feb-26 08:00	06-Jul-26 17:00	17-Feb-26 08:00 A	01-Sep-26 11:12 A	0.00	0.00	0.00	0%	0%	-48
	LONG LEAD ITEMS	163	21-Feb-26 08:00	06-Jul-26 17:00	21-Feb-26 08:00 A	01-Sep-26 11:12 A	0.00	0.00	0.00	0%	0%	-48
	EXTERNAL / LANDSCAPE WORK	56	25-Feb-26 08:00	06-May-26 10:00	25-Feb-26 08:00 A	05-May-26 17:00 A	0.00	0.00	0.00	0%	0%	0
	SPORTS & RECREATIONAL FACILITIES WORK	47	08-Mar-26 08:00	06-May-26 10:00	08-Mar-26 08:00 A	05-May-26 17:00 A	0.00	0.00	0.00	0%	0%	0
	CONCRETE WORK	41	07-Mar-26 08:00	28-Apr-26 10:00	07-Mar-26 08:00 A	27-Apr-26 17:00 A	0.00	0.00	0.00	0%	0%	0
	METAL WORK	44	11-Mar-26 08:00	06-May-26 10:00	11-Mar-26 08:00 A	05-May-26 17:00 A	0.00	0.00	0.00	0%	0%	0
	PLUMBING WORK	44	11-Mar-26 08:00	06-May-26 10:00	11-Mar-26 08:00 A	05-May-26 17:00 A	0.00	0.00	0.00	0%	0%	0
	IRRIGATION WORK	60	21-Feb-26 08:00	07-May-26 10:00	21-Feb-26 08:00 A	06-May-26 17:00 A	0.00	0.00	0.00	0%	0%	0
	ELECTRICAL WORK	99	12-May-26 08:00	06-Jul-26 17:00	12-May-26 08:00 A	01-Sep-26 11:12 A	0.00	0.00	0.00	0%	0%	-48
	SHORT LEAD ITEMS	28	17-Feb-26 08:00	28-Mar-26 10:00	17-Feb-26 08:00 A	26-Mar-26 17:00 A	0.00	0.00	0.00	0%	0%	0
	EXTERNAL / LANDSCAPE WORK	23	17-Feb-26 08:00	17-Mar-26 10:00	17-Feb-26 08:00 A	16-Mar-26 17:00 A	0.00	0.00	0.00	0%	0%	0
	CONCRETE WORK	28	17-Feb-26 08:00	28-Mar-26 10:00	17-Feb-26 08:00 A	26-Mar-26 17:00 A	0.00	0.00	0.00	0%	0%	0
	ARCHITECTURAL & FINISHES WORK	4	10-Mar-26 08:00	15-Mar-26 10:00	10-Mar-26 08:00 A	14-Mar-26 17:00 A	0.00	0.00	0.00	0%	0%	0
	METAL WORK	9	07-Mar-26 08:00	17-Mar-26 10:00	07-Mar-26 08:00 A	16-Mar-26 17:00 A	0.00	0.00	0.00	0%	0%	0
	HVAC WORK	19	23-Feb-26 08:00	17-Mar-26 10:00	23-Feb-26 08:00 A	16-Mar-26 17:00 A	0.00	0.00	0.00	0%	0%	0
	PLUMBING WORK	4	12-Mar-26 08:00	17-Mar-26 10:00	12-Mar-26 08:00 A	16-Mar-26 17:00 A	0.00	0.00	0.00	0%	0%	0
	IRRIGATION WORK	4	12-Mar-26 08:00	17-Mar-26 10:00	12-Mar-26 08:00 A	16-Mar-26 17:00 A	0.00	0.00	0.00	0%	0%	0
	ELECTRICAL WORK	4	12-Mar-26 08:00	17-Mar-26 10:00	12-Mar-26 08:00 A	16-Mar-26 17:00 A	0.00	0.00	0.00	0%	0%	0
	FIRE FIGHTING WORK	4	12-Mar-26 08:00	17-Mar-26 10:00	12-Mar-26 08:00 A	16-Mar-26 17:00 A	0.00	0.00	0.00	0%	0%	0
	MATERIAL APPROVALS	165	21-Feb-26 08:00	14-Jul-26 17:00	21-Feb-26 08:00 A	17-Sep-26 17:00 A	204,439.56	204,439.56	204,439.56	100%	100%	-56
	LONG LEAD ITEMS	162	25-Feb-26 08:00	14-Jul-26 17:00	25-Feb-26 08:00 A	17-Sep-26 17:00 A	111,065.49	111,065.49	111,065.49	100%	100%	-56
	EXTERNAL / LANDSCAPE WORK	57	25-Feb-26 08:00	06-May-26 17:00	25-Feb-26 08:00 A	06-May-26 17:00 A	26,079.63	26,079.63	26,079.63	100%	100%	0
	SPORTS & RECREATIONAL FACILITIES WORK	43	14-Mar-26 08:00	06-May-26 17:00	14-Mar-26 08:00 A	06-May-26 17:00 A	38,839.50	38,839.50	38,839.50	100%	100%	0
	CONCRETE WORK	45	11-Mar-26 08:00	06-May-26 17:00	11-Mar-26 08:00 A	06-May-26 17:00 A	1,417.50	1,417.50	1,417.50	100%	100%	0
	METAL WORK	42	15-Mar-26 08:00	06-May-26 17:00	15-Mar-26 08:00 A	06-May-26 17:00 A	889.23	889.23	889.23	100%	100%	0
	PLUMBING WORK	41	16-Mar-26 08:00	06-May-26 17:00	16-Mar-26 08:00 A	06-May-26 17:00 A	3,553.95	3,553.95	3,553.95	100%	100%	0
	IRRIGATION WORK	55	28-Feb-26 08:00	06-May-26 17:00	28-Feb-26 08:00 A	06-May-26 17:00 A	12,818.25	12,818.25	12,818.25	100%	100%	0
	ELECTRICAL WORK	101	12-May-26 08:00	14-Jul-26 17:00	12-May-26 08:00 A	17-Sep-26 17:00 A	27,467.43	27,467.43	27,467.43	100%	100%	-56
	SHORT LEAD ITEMS	25	21-Feb-26 08:00	26-Mar-26 17:00	21-Feb-26 08:00 A	26-Mar-26 17:00 A	93,374.07	93,374.07	93,374.07	100%	100%	0
	EXTERNAL / LANDSCAPE WORK	25	21-Feb-26 08:00	26-Mar-26 17:00	21-Feb-26 08:00 A	26-Mar-26 17:00 A	72,133.44	72,133.44	72,133.44	100%	100%	0
	CONCRETE WORK	24	23-Feb-26 08:00	26-Mar-26 17:00	23-Feb-26 08:00 A	26-Mar-26 17:00 A	1,609.47	1,609.47	1,609.47	100%	100%	0
	ARCHITECTURAL & FINISHES WORK	2	15-Mar-26 08:00	16-Mar-26 17:00	15-Mar-26 08:00 A	16-Mar-26 17:00 A	8,114.01	8,114.01	8,114.01	100%	100%	0
	METAL WORK	10	11-Mar-26 08:00	26-Mar-26 17:00	11-Mar-26 08:00 A	26-Mar-26 17:00 A	478.89	478.89	478.89	100%	100%	0
	HVAC WORK	20	28-Feb-26 08:00	26-Mar-26 17:00	28-Feb-26 08:00 A	26-Mar-26 17:00 A	606.36	606.36	606.36	100%	100%	0
	PLUMBING WORK	2	25-Mar-26 08:00	26-Mar-26 17:00	25-Mar-26 08:00 A	26-Mar-26 17:00 A	3,147.03	3,147.03	3,147.03	100%	100%	0
	IRRIGATION WORK	2	25-Mar-26 08:00	26-Mar-26 17:00	25-Mar-26 08:00 A	26-Mar-26 17:00 A	6,854.64	6,854.64	6,854.64	100%	100%	0
	ELECTRICAL WORK	2	25-Mar-26 08:00	26-Mar-26 17:00	25-Mar-26 08:00 A	26-Mar-26 17:00 A	407.52	407.52	407.52	100%	100%	0
	FIRE FIGHTING WORK	2	25-Mar-26 08:00	26-Mar-26 17:00	25-Mar-26 08:00 A	26-Mar-26 17:00 A	22.71	22.71	22.71	100%	100%	0
	PROCUREMENT	215	26-Feb-26 08:00	26-Aug-26 17:00	26-Feb-26 08:00 A	26-Oct-26 11:12	1,839,956.04	1,816,202.83	1,839,956.04	100%	98.71%	-50
	LONG LEAD ITEMS	209	05-Mar-26 08:00	26-Aug-26 17:00	05-Mar-26 08:00 A	26-Oct-26 11:12	999,589.41	981,462.29	999,589.41	100%	98.19%	-50
	PURCHASE ORDER	162	05-Mar-26 08:00	22-Jul-26 17:00	05-Mar-26 08:00 A	08-Sep-26 11:36 A	0.00	0.00	0.00	0%	0%	-40
	EXTERNAL / LANDSCAPE WORK	49	07-Mar-26 08:00	07-May-26 10:00	07-Mar-26 08:00 A	06-May-26 17:00 A	0.00	0.00	0.00	0%	0%	0
	SPORTS & RECREATIONAL FACILITIES WORK	35	28-Mar-26 08:00	07-May-26 10:00	28-Mar-26 08:00 A	06-May-26 17:00 A	0.00	0.00	0.00	0%	0%	0
	CONCRETE WORK	39	18-Mar-26 08:00	07-May-26 10:00	18-Mar-26 08:00 A	06-May-26 17:00 A	0.00	0.00	0.00	0%	0%	0
	METAL WORK	38	24-Mar-26 08:00	07-May-26 10:00	24-Mar-26 08:00 A	06-May-26 17:00 A	0.00	0.00	0.00	0%	0%	0
	PLUMBING WORK	34	29-Mar-26 08:00	07-May-26 10:00	29-Mar-26 08:00 A	06-May-26 17:00 A	0.00	0.00	0.00	0%	0%	0
	IRRIGATION WORK	50	05-Mar-26 08:00	07-May-26 10:00	05-Mar-26 08:00 A	06-May-26 17:00 A	0.00	0.00	0.00	0%	0%	0
	ELECTRICAL WORK	109	11-May-26 08:00	22-Jul-26 17:00	11-May-26 08:00 A	08-Sep-26 11:36 A	0.00	0.00	0.00	0%	0%	-40
	MANUFACTURE / FABRICATION	190	01-Apr-26 08:00	12-Aug-26 17:00	01-Apr-26 08:00 A	02-Oct-26 17:00 A	0.00	0.00	0.00	0%	0%	-42
	EXTERNAL / LANDSCAPE WORK	103	05-May-26 08:00	23-Jul-26 17:00	05-May-26 08:00 A	10-Sep-26 08:00 A	0.00	0.00	0.00	0%	0%	-41
	SPORTS & RECREATIONAL FACILITIES WORK	97	05-May-26 08:00	23-Jul-26 17:00	05-May-26 08:00 A	10-Sep-26 08:00 A	0.00	0.00	0.00	0%	0%	-41
	CONCRETE WORK	93	01-Apr-26 08:00	06-Jul-26 17:00	01-Apr-26 08:00 A	27-Jun-26 17:00 A	0.00	0.00	0.00	0%	0%	8
	METAL WORK	161	05-May-26 08:00	23-Jul-26 17:00	05-May-26 08:00 A	02-Oct-26 17:00 A	0.00	0.00	0.00	0%	0%	-59
	PLUMBING WORK	120	05-May-26 08:00	23-Jul-26 17:00	05-May-26 08:00 A	10-Sep-26 08:00 A	0.00	0.00	0.00	0%	0%	-41
	IRRIGATION WORK	107	05-May-26 08:00	08-Jul-26 17:00	05-May-26 08:00 A	10-Sep-26 08:00 A	0.00	0.00	0.00	0%	0%	-54
	ELECTRICAL WORK	131	12-May-26 08:00	12-Aug-26 17:00	12-May-26 08:00 A	10-Sep-26 12:00 A	0.00	0.00	0.00	0%	0%	-25
	DELIVERY TO SITE	147	07-May-26 08:00	26-Aug-26 17:00	06-May-26 17:00 A	26-Oct-26 11:12	999,589.41	981,462.29	999,589.41	100%	98.19%	-50
	EXTERNAL / LANDSCAPE WORK	118	07-May-26 08:00	06-Aug-26 17:00	06-May-26 17:00 A	15-Oct-26 17:00 A	234,716.67	234,716.67	234,716.67	100%	100%	-59
	SPORTS & RECREATIONAL FACILITIES WORK	106	07-May-26 08:00	06-Aug-26 17:00	06-May-26 17:00 A	15-Oct-26 17:00 A	349,555.50	349,555.50	349,555.50	100%	100%	-59
	CONCRETE WORK	67	07-May-26 08:00	12-Jul-26 17:00	06-May-26 17:00 A	07-Jul-26 17:00 A	12,757.50	12,757.50	12,757.50	100%	100%	4

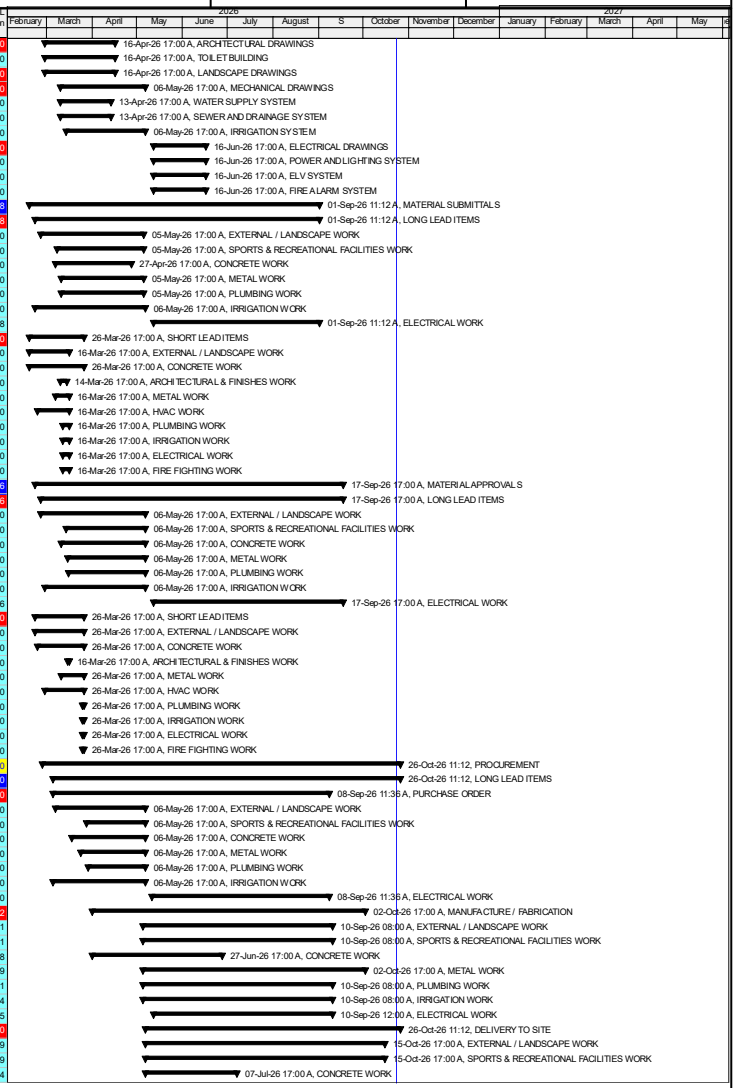


Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining W...
Milestone
summary

Baseline Schedule Rev.00

PLAYGROUNDS INITIATIVE - QASSIM, HAIL & TABUK - 25-Oct-2026

Activity ID	Activity Name	O.D	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Schedule % Complete	Performance % Complete	Variance - BL Project Duration
	METAL WORK	130	07-May-26 08:00	06-Aug-26 17:00	06-May-26 17:00 A	26-Oct-26 11:12	8,003.07	7,180.43	8,003.07	100%	89.72%	-67
	PLUMBING WORK	130	07-May-26 08:00	06-Aug-26 17:00	06-May-26 17:00 A	15-Oct-26 17:00 A	31,985.55	31,985.55	31,985.55	100%	100%	-59
	IRRIGATION WORK	108	07-May-26 08:00	18-Jul-26 17:00	06-May-26 17:00 A	04-Sep-26 12:48 A	115,364.25	115,364.25	115,364.25	100%	100%	-41
	ELECTRICAL WORK	142	13-May-26 08:00	26-Aug-26 17:00	13-May-26 08:00 A	25-Oct-26 09:36	247,206.87	229,902.39	247,206.87	100%	93%	-49
	SHORT LEAD ITEMS	196	26-Feb-26 08:00	16-Jul-26 17:00	26-Feb-26 08:00 A	25-Oct-26 09:36	840,366.63	834,740.53	840,366.63	100%	99.33%	-84
	PURCHASE ORDER	156	26-Feb-26 08:00	02-Jul-26 17:00	26-Feb-26 08:00 A	27-Aug-26 17:00 A	0.00	0.00	0.00	0%	0%	-48
	EXTERNAL / LANDSCAPE WORK	156	26-Feb-26 08:00	02-Jul-26 17:00	26-Feb-26 08:00 A	27-Aug-26 17:00 A	0.00	0.00	0.00	0%	0%	-48
	CONCRETE WORK	41	02-Mar-26 08:00	23-Apr-26 10:00	02-Mar-26 08:00 A	22-Apr-26 17:00 A	0.00	0.00	0.00	0%	0%	0
	ARCHITECTURAL & FINISHES WORK	7	05-May-26 08:00	13-May-26 10:00	05-May-26 08:00 A	12-May-26 17:00 A	0.00	0.00	0.00	0%	0%	0
	METAL WORK	7	05-May-26 08:00	13-May-26 10:00	05-May-26 08:00 A	12-May-26 17:00 A	0.00	0.00	0.00	0%	0%	0
	HVAC WORK	7	05-May-26 08:00	13-May-26 10:00	05-May-26 08:00 A	12-May-26 17:00 A	0.00	0.00	0.00	0%	0%	0
	PLUMBING WORK	7	05-May-26 08:00	13-May-26 10:00	05-May-26 08:00 A	12-May-26 17:00 A	0.00	0.00	0.00	0%	0%	0
	IRRIGATION WORK	102	05-May-26 08:00	02-Jul-26 17:00	05-May-26 08:00 A	27-Aug-26 17:00 A	0.00	0.00	0.00	0%	0%	-48
	ELECTRICAL WORK	96	12-May-26 08:00	02-Jul-26 17:00	12-May-26 08:00 A	27-Aug-26 17:00 A	0.00	0.00	0.00	0%	0%	-48
	FIRE FIGHTING WORK	96	12-May-26 08:00	02-Jul-26 17:00	12-May-26 08:00 A	27-Aug-26 17:00 A	0.00	0.00	0.00	0%	0%	-48
	DELIVERY TO SITE	194	01-Mar-26 08:00	16-Jul-26 17:00	01-Mar-26 08:00 A	25-Oct-26 09:36	840,366.63	834,740.53	840,366.63	100%	99.33%	-84
	EXTERNAL / LANDSCAPE WORK	166	01-Mar-26 08:00	16-Jul-26 17:00	01-Mar-26 08:00 A	25-Oct-26 09:36	649,200.96	643,574.86	649,200.96	100%	99.13%	-84
	CONCRETE WORK	52	10-Mar-26 08:00	13-May-26 17:00	10-Mar-26 08:00 A	13-May-26 17:00 A	14,485.23	14,485.23	14,485.23	100%	100%	0
	ARCHITECTURAL & FINISHES WORK	6	06-May-26 08:00	12-May-26 17:00	06-May-26 08:00 A	12-May-26 17:00 A	73,026.09	73,026.09	73,026.09	100%	100%	0
	METAL WORK	6	06-May-26 08:00	12-May-26 17:00	06-May-26 08:00 A	12-May-26 17:00 A	4,310.01	4,310.01	4,310.01	100%	100%	0
	HVAC WORK	6	06-May-26 08:00	12-May-26 17:00	06-May-26 08:00 A	12-May-26 17:00 A	5,457.24	5,457.24	5,457.24	100%	100%	0
	PLUMBING WORK	6	06-May-26 08:00	12-May-26 17:00	06-May-26 08:00 A	12-May-26 17:00 A	28,323.27	28,323.27	28,323.27	100%	100%	0
	IRRIGATION WORK	113	06-May-26 08:00	16-Jul-26 17:00	06-May-26 08:00 A	15-Oct-26 17:00 A	61,691.76	61,691.76	61,691.76	100%	100%	-77
	ELECTRICAL WORK	117	20-May-26 08:00	16-Jul-26 17:00	20-May-26 08:00 A	15-Oct-26 17:00 A	3,667.68	3,667.68	3,667.68	100%	100%	-77
	FIRE FIGHTING WORK	129	20-May-26 08:00	16-Jul-26 17:00	20-May-26 08:00 A	15-Oct-26 17:00 A	204.39	204.39	204.39	100%	100%	-77
	CONSTRUCTION STAGE	237	05-Apr-26 08:00	26-Nov-26 17:00	05-Apr-26 08:00 A	21-Dec-26 14:36	3,941,913.75	3,560,642.09	4,088,791.20	96.41%	87.08%	-21
	PLAYGROUND AND LANDSCAPING WORKS	237	05-Apr-26 08:00	26-Nov-26 17:00	05-Apr-26 08:00 A	21-Dec-26 14:36	3,613,420.17	3,286,366.22	3,760,297.62	96.09%	87.4%	-21
	CUT AND FILL	28	05-Apr-26 08:00	06-May-26 17:00	05-Apr-26 08:00 A	06-May-26 17:00 A	453,900.00	453,900.00	453,900.00	100%	100%	0
	PLAYGROUND WORKS	177	19-Apr-26 08:00	17-Nov-26 17:00	19-Apr-26 08:00 A	16-Nov-26 12:48	754,153.08	701,267.82	781,940.40	96.45%	89.68%	1
	FOOTBALL PLAYGROUND WORKS	177	19-Apr-26 08:00	17-Nov-26 17:00	19-Apr-26 08:00 A	16-Nov-26 12:48	754,153.08	701,267.82	781,940.40	96.45%	89.68%	1
	GENERAL SITE WORKS	227	16-Apr-26 08:00	26-Nov-26 17:00	16-Apr-26 08:00 A	21-Dec-26 14:36	1,217,232.42	1,003,799.83	1,224,114.42	99.44%	82%	-21
	FENCE WORKS	159	16-Apr-26 08:00	16-Aug-26 17:00	16-Apr-26 08:00 A	15-Oct-26 17:00 A	65,818.80	65,818.80	65,818.80	100%	100%	-51
	MECHANICAL WORK	152	12-May-26 08:00	06-Aug-26 17:00	12-May-26 08:00 A	09-Nov-26 10:24	421,027.74	358,530.44	421,027.74	100%	85.16%	-79
	STORM WATER AND UTILITY WORK	150	12-May-26 08:00	04-Aug-26 17:00	12-May-26 08:00 A	08-Nov-26 12:00	27,252.00	18,292.80	27,252.00	100%	67.12%	-81
	IRRIGATION SYSTEM WORKS	132	02-Jun-26 09:36	30-Jul-26 17:00	02-Jun-26 09:36 A	03-Nov-26 12:00	393,457.80	340,046.88	393,457.80	100%	86.43%	-81
	FIRE PROTECTION SYSTEM	2	05-Aug-26 08:00	06-Aug-26 17:00	11-Oct-26 08:00 A	09-Nov-26 10:24	317.94	190.76	317.94	100%	60%	-23
	ELECTRICAL WORK	198	20-May-26 08:00	20-Oct-26 17:00	20-May-26 08:00 A	05-Dec-26 10:24	539,251.68	418,854.59	539,251.68	100%	77.67%	-38
	POWER, LIGHTING & GROUNDING	163	20-May-26 08:00	08-Sep-26 17:00	20-May-26 08:00 A	18-Nov-26 10:24	482,181.48	384,612.47	482,181.48	100%	79.77%	-59
	ELV SYSTEMS (TELECOM, DATA, AV & CCTV)	25	09-Sep-26 08:00	08-Oct-26 17:00	10-Oct-26 08:00 A	30-Nov-26 10:24	43,146.00	25,887.60	43,146.00	100%	60%	-19
	FIRE ALARM SYSTEM	32	13-Sep-26 08:00	20-Oct-26 17:00	10-Oct-26 08:00 A	05-Dec-26 10:24	13,924.20	8,354.52	13,924.20	100%	60%	-16
	PARKING WORK	147	17-Jun-26 08:00	20-Oct-26 17:00	17-Jun-26 08:00 A	07-Dec-26 10:24	190,576.20	155,574.00	190,576.20	100%	81.63%	-40
	SERVICE CONNECTION	23	21-Oct-26 08:00	26-Nov-26 17:00	30-Jul-26 08:00 A	21-Dec-26 14:36	558.00	5,022.00	7,440.00	7.5%	67.5%	-91
	LANDSCAPING WORKS	163	31-May-26 08:00	09-Nov-26 17:00	30-May-26 16:12 A	07-Dec-26 12:48	1,139,844.27	1,100,356.27	1,252,052.40	91.04%	87.88%	-24
	HARDSCAPE WORK	163	31-May-26 08:00	09-Nov-26 17:00	30-May-26 16:12 A	07-Dec-26 12:48	988,605.27	1,002,076.27	1,046,213.40	94.49%	95.78%	-24
	SOFTSCAPE WORK	155	03-Jun-26 10:00	09-Nov-26 17:00	03-Jun-26 10:00 A	07-Dec-26 12:48	151,239.00	98,280.00	205,839.00	73.47%	47.75%	-24
	TANK WORKS	148	13-May-26 08:00	19-Sep-26 17:00	13-May-26 08:00 A	10-Nov-26 17:00	48,290.40	27,042.30	48,290.40	100%	56%	-44
	SEPTIC TANK	148	13-May-26 08:00	31-Aug-26 17:00	13-May-26 08:00 A	07-Nov-26 17:00	7,475.22	7,054.92	7,475.22	100%	94.38%	-57
	WATER STORAGE TANK	148	13-May-26 08:00	19-Sep-26 17:00	13-May-26 08:00 A	10-Nov-26 17:00	40,815.18	19,987.38	40,815.18	100%	48.97%	-44
	TOILET BUILDING WORKS	165	12-May-26 08:00	12-Oct-26 17:00	12-May-26 08:00 A	05-Nov-26 16:36	328,493.58	274,275.86	328,493.58	100%	83.5%	-21
	CIVIL WORK	165	12-May-26 08:00	12-Oct-26 17:00	12-May-26 08:00 A	04-Nov-26 16:36	230,766.78	192,413.10	230,766.78	100%	83.38%	-20
	STRUCTURAL WORK	59	12-May-26 08:00	22-Jul-26 17:00	12-May-26 08:00 A	23-Jul-26 17:00 A	37,980.00	37,980.00	37,980.00	100%	100%	-1
	ARCHITECTURAL WORK	99	23-Jul-26 08:00	12-Oct-26 17:00	31-Jul-26 08:00 A	04-Nov-26 16:36	192,786.78	154,433.10	192,786.78	100%	80.11%	-13
	GENERAL FINISHES	99	23-Jul-26 08:00	12-Oct-26 17:00	31-Jul-26 08:00 A	04-Nov-26 16:36	87,769.20	62,097.24	87,769.20	100%	70.75%	-13
	WET AREA FINISHES	61	12-Aug-26 08:00	11-Oct-26 17:00	07-Aug-26 08:00 A	31-Oct-26 12:24	81,123.78	80,051.46	81,123.78	100%	98.68%	-21
	ROOF FINISHES	39	19-Sep-26 08:00	05-Oct-26 17:00	20-Aug-26 08:00 A	04-Nov-26 16:36	23,893.80	12,284.40	23,893.80	100%	51.41%	-51
	MEP WORK	75	28-Jul-26 08:00	06-Oct-26 17:00	22-Jul-26 08:00 A	05-Nov-26 16:36	97,726.80	81,862.76	97,726.80	100%	83.77%	-31
	MECANICAL WORKS	75	28-Jul-26 08:00	06-Oct-26 17:00	22-Jul-26 08:00 A	05-Nov-26 16:36	79,479.48	66,055.00	79,479.48	100%	83.11%	-31
	FIRE FIGHTING SYSTEM	1	06-Oct-26 08:00	06-Oct-26 17:00	04-Nov-26 16:36	05-Nov-26 16:36	136.26	0.00	136.26	100%	0%	0
	SEWER AND DRAINAGE SYSTEM	65	03-Aug-26 08:00	23-Aug-26 17:00	22-Jul-26 08:00 A	27-Oct-26 12:00	11,290.02	7,580.44	11,290.02	100%	67.14%	-65
	HVAC SYSTEM	31	28-Jul-26 08:00	15-Aug-26 17:00	13-Aug-26 08:00 A	24-Oct-26 16:12	12,127.20	9,821.76	12,127.20	100%	80.99%	-45
	WATER SUPPLY SYSTEM	56	01-Aug-26 08:00	20-Aug-26 17:00	30-Jul-26 08:00 A	25-Oct-26 12:00	55,926.00	48,652.80	55,926.00	100%	86.99%	-56
	ELECTRICAL WORKS	40	05-Aug-26 08:00	08-Sep-26 17:00	12-Aug-26 08:00 A	29-Oct-26 09:12	18,247.32	15,807.76	18,247.32	100%	86.63%	-36
	PROJECT CLOSOUT	191	25-May-26 09:36	15-Dec-26 17:00	25-May-26 09:36 A	09-Jan-27 12:48	20,443.96	94,042.20	681,465.20	3%	13.8%	-21
	TABUK	299	17-Feb-26 08:00	16-Dec-26 17:00	17-Feb-26 08:00 A	11-Feb-27 17:00	8,880,320.41	6,802,182.48	11,357,801.00	78.19%	59.89%	-49
	MOBILIZATION	44	17-Feb-26 08:00	15-Apr-26 10:00	17-Feb-26 08:00 A	14-Apr-26 17:00 A	0.00	0.00	0.00	0%	0%	0
	TEMPORARY CAMP	43	17-Feb-26 08:00	14-Apr-26 10:00	17-Feb-26 08:00 A	13-Apr-26 17:00 A	0.00	0.00	0.00	0%	0%	0
	SITE OFFICES	44	17-Feb-26 08:00	15-Apr-26 10:00	17-Feb-26 08:00 A	14-Apr-26 17:00 A	0.00	0.00	0.00	0%	0%	0
	GENERAL REQUIEREMENTS	44	17-Feb-26 08:00	15-Apr-26 10:00	17-Feb-26 08:00 A	14-Apr-26 17:00 A	0.00	0.00	0.00	0%	0%	0
	ENGINEERING	171	17-Feb-26 08:00	12-Aug-26 17:00	17-Feb-26 08:00 A	17-Sep-26 11:12 A	340,734.03	340,734.03	340,734.03	100%	100%	-30
	SHOP DRAWINGS SUBMITTALS	163	17-Feb-26 08:00	04-Aug-26 17:00	17-Feb-26 08:00 A	10-Sep-26 10:00 A	0.00	0.00	0.00	0%	0%	-31
	STRUCTURAL DRAWINGS	135	17-Feb-26 08:00	18-Jul-26 17:00	17-Feb-26 08:00 A	03-Jul-26 17:00 A	0.00	0.00	0.00	0%	0%	13

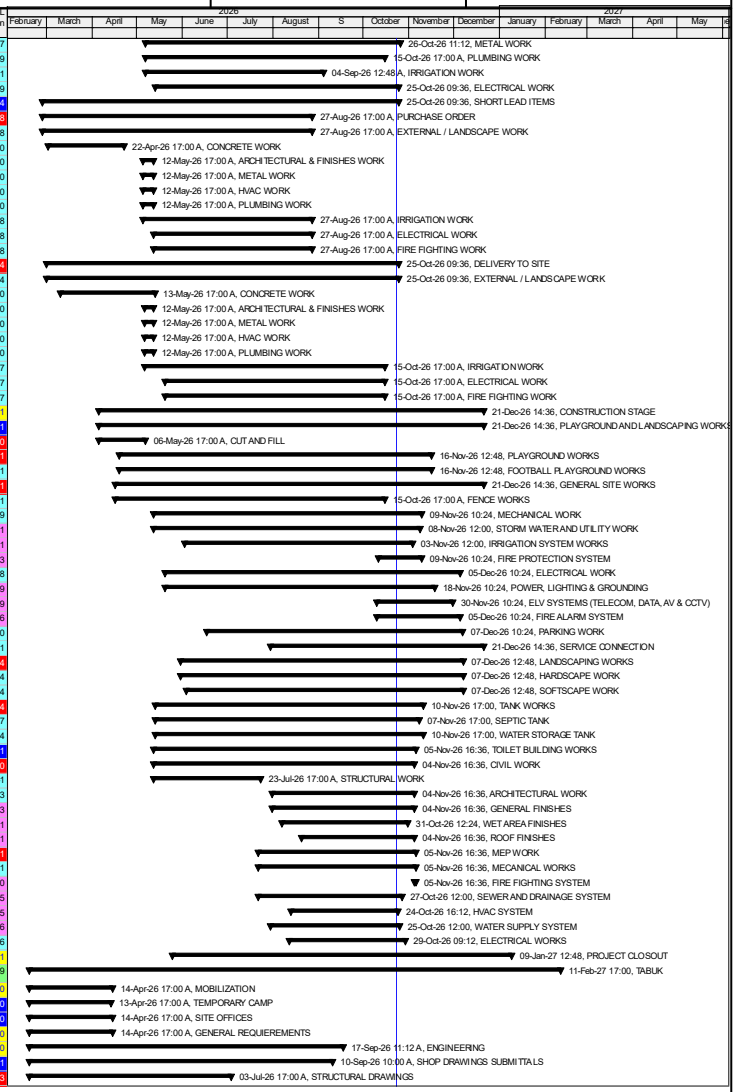


Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining W...
Milestone
summary

Baseline Schedule Rev.00

PLAYGROUNDS INITIATIVE - QASSIM, HAIL & TABUK - 25-Oct-2026

Activity ID	Activity Name	O.D	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Schedule % Complete	Performance % Complete	Variance - BL Project Duration
	PROJECT FENCE	63	17-Feb-26 08:00	07-May-26 10:00	17-Feb-26 08:00 A	06-May-26 17:00 A	0.00	0.00	0.00	0%	0%	0
	PADEL PLAYGROUND FENCE	63	17-Feb-26 08:00	07-May-26 10:00	17-Feb-26 08:00 A	06-May-26 17:00 A	0.00	0.00	0.00	0%	0%	0
	AIR DOME	20	25-Jun-26 08:00	18-Jul-26 17:00	01-Jul-26 08:00 A	03-Jul-26 17:00 A	0.00	0.00	0.00	0%	0%	18
	TOILET BUILDING	41	19-Feb-26 08:00	14-Apr-26 10:00	19-Feb-26 08:00 A	13-Apr-26 17:00 A	0.00	0.00	0.00	0%	0%	0
	WATER STORAGE TANK	39	23-Feb-26 08:00	14-Apr-26 10:00	23-Feb-26 08:00 A	13-Apr-26 17:00 A	0.00	0.00	0.00	0%	0%	0
	SEPTIC TANK	57	25-Feb-26 08:00	07-May-26 10:00	25-Feb-26 08:00 A	06-May-26 17:00 A	0.00	0.00	0.00	0%	0%	0
	ARCHITECTURAL DRAWINGS	150	23-Feb-26 08:00	04-Aug-26 17:00	23-Feb-26 08:00 A	10-Sep-26 10:00 A	0.00	0.00	0.00	0%	0%	-31
	TOILET BUILDING	40	23-Feb-26 08:00	15-Apr-26 10:00	23-Feb-26 08:00 A	14-Apr-26 17:00 A	0.00	0.00	0.00	0%	0%	0
	AIR DOME	15	19-Jul-26 08:00	04-Aug-26 17:00	05-Aug-26 08:00 A	10-Sep-26 10:00 A	0.00	0.00	0.00	0%	0%	-16
	LANDSCAPE DRAWINGS	40	23-Feb-26 08:00	15-Apr-26 10:00	23-Feb-26 08:00 A	14-Apr-26 17:00 A	0.00	0.00	0.00	0%	0%	0
	MECHANICAL DRAWINGS	140	28-Feb-26 08:00	12-Jul-26 17:00	28-Feb-26 08:00 A	13-Jul-26 17:00 A	0.00	0.00	0.00	0%	0%	-1
	WATER SUPPLY SYSTEM	32	28-Feb-26 08:00	11-Apr-26 10:00	28-Feb-26 08:00 A	09-Apr-26 17:00 A	0.00	0.00	0.00	0%	0%	0
	SEWER AND DRAINAGE SYSTEM	28	04-Mar-26 08:00	11-Apr-26 10:00	04-Mar-26 08:00 A	09-Apr-26 17:00 A	0.00	0.00	0.00	0%	0%	0
	IRRIGATION SYSTEM	47	09-Mar-26 08:00	07-May-26 10:00	09-Mar-26 08:00 A	06-May-26 17:00 A	0.00	0.00	0.00	0%	0%	0
	AIR DOME	15	25-Jun-26 08:00	12-Jul-26 17:00	02-Jul-26 08:00 A	13-Jul-26 17:00 A	0.00	0.00	0.00	0%	0%	5
	ELECTRICAL DRAWINGS	98	10-May-26 08:00	29-Jul-26 17:00	10-May-26 08:00 A	12-Jul-26 17:00 A	0.00	0.00	0.00	0%	0%	15
	POWER AND LIGHTING SYSTEM	10	10-May-26 08:00	21-May-26 10:00	10-May-26 08:00 A	20-May-26 17:00 A	0.00	0.00	0.00	0%	0%	0
	ELV SYSTEM	10	10-May-26 08:00	21-May-26 10:00	10-May-26 08:00 A	20-May-26 17:00 A	0.00	0.00	0.00	0%	0%	0
	FIRE ALARM SYSTEM	10	10-May-26 08:00	21-May-26 10:00	10-May-26 08:00 A	20-May-26 17:00 A	0.00	0.00	0.00	0%	0%	0
	AIR DOME	30	25-Jun-26 08:00	29-Jul-26 17:00	08-Jul-26 08:00 A	12-Jul-26 17:00 A	0.00	0.00	0.00	0%	0%	26
	SHOP DRAWINGS APPROVALS	169	19-Feb-26 08:00	12-Aug-26 17:00	19-Feb-26 08:00 A	02-Sep-26 15:00 A	0.00	0.00	0.00	0%	0%	-18
	STRUCTURAL DRAWINGS	138	19-Feb-26 08:00	23-Jul-26 17:00	19-Feb-26 08:00 A	11-Jul-26 08:00 A	0.00	0.00	0.00	0%	0%	12
	PROJECT FENCE	61	19-Feb-26 08:00	07-May-26 10:00	19-Feb-26 08:00 A	06-May-26 17:00 A	0.00	0.00	0.00	0%	0%	0
	PADEL PLAYGROUND FENCE	61	19-Feb-26 08:00	07-May-26 10:00	19-Feb-26 08:00 A	06-May-26 17:00 A	0.00	0.00	0.00	0%	0%	0
	AIR DOME	15	07-Jul-26 08:00	23-Jul-26 17:00	05-Jul-26 08:00 A	11-Jul-26 08:00 A	0.00	0.00	0.00	0%	0%	10
	TOILET BUILDING	42	23-Feb-26 08:00	18-Apr-26 10:00	23-Feb-26 08:00 A	16-Apr-26 17:00 A	0.00	0.00	0.00	0%	0%	0
	WATER STORAGE TANK	40	25-Feb-26 08:00	18-Apr-26 10:00	25-Feb-26 08:00 A	16-Apr-26 17:00 A	0.00	0.00	0.00	0%	0%	0
	SEPTIC TANK	54	01-Mar-26 08:00	07-May-26 10:00	01-Mar-26 08:00 A	06-May-26 17:00 A	0.00	0.00	0.00	0%	0%	0
	ARCHITECTURAL DRAWINGS	153	28-Feb-26 08:00	12-Aug-26 17:00	28-Feb-26 08:00 A	02-Sep-26 15:00 A	0.00	0.00	0.00	0%	0%	-18
	TOILET BUILDING	38	28-Feb-26 08:00	18-Apr-26 10:00	28-Feb-26 08:00 A	16-Apr-26 17:00 A	0.00	0.00	0.00	0%	0%	0
	AIR DOME	7	05-Aug-26 08:00	12-Aug-26 17:00	06-Aug-26 08:00 A	02-Sep-26 15:00 A	0.00	0.00	0.00	0%	0%	-17
	LANDSCAPE DRAWINGS	39	26-Feb-26 08:00	18-Apr-26 10:00	26-Feb-26 08:00 A	16-Apr-26 17:00 A	0.00	0.00	0.00	0%	0%	0
	MECHANICAL DRAWINGS	142	09-Mar-26 08:00	23-Jul-26 17:00	09-Mar-26 08:00 A	18-Jul-26 17:00 A	0.00	0.00	0.00	0%	0%	5
	WATER SUPPLY SYSTEM	27	09-Mar-26 08:00	14-Apr-26 10:00	09-Mar-26 08:00 A	13-Apr-26 17:00 A	0.00	0.00	0.00	0%	0%	0
	SEWER AND DRAINAGE SYSTEM	27	09-Mar-26 08:00	14-Apr-26 10:00	09-Mar-26 08:00 A	13-Apr-26 17:00 A	0.00	0.00	0.00	0%	0%	0
	IRRIGATION SYSTEM	44	12-Mar-26 08:00	07-May-26 10:00	12-Mar-26 08:00 A	06-May-26 17:00 A	0.00	0.00	0.00	0%	0%	0
	AIR DOME	10	13-Jul-26 08:00	23-Jul-26 17:00	13-Jul-26 08:00 A	18-Jul-26 17:00 A	0.00	0.00	0.00	0%	0%	5
	ELECTRICAL DRAWINGS	105	11-May-26 08:00	08-Aug-26 17:00	11-May-26 08:00 A	19-Jul-26 17:00 A	0.00	0.00	0.00	0%	0%	17
	POWER AND LIGHTING SYSTEM	28	11-May-26 08:00	17-Jun-26 10:00	11-May-26 08:00 A	16-Jun-26 17:00 A	0.00	0.00	0.00	0%	0%	0
	ELV SYSTEM	28	11-May-26 08:00	17-Jun-26 10:00	11-May-26 08:00 A	16-Jun-26 17:00 A	0.00	0.00	0.00	0%	0%	0
	FIRE ALARM SYSTEM	28	11-May-26 08:00	17-Jun-26 10:00	11-May-26 08:00 A	16-Jun-26 17:00 A	0.00	0.00	0.00	0%	0%	0
	AIR DOME	23	13-Jul-26 08:00	08-Aug-26 17:00	13-Jul-26 08:00 A	19-Jul-26 17:00 A	0.00	0.00	0.00	0%	0%	17
	MATERIAL SUBMITTALS	166	17-Feb-26 08:00	11-Jul-26 17:00	17-Feb-26 08:00 A	15-Sep-26 12:00 A	0.00	0.00	0.00	0%	0%	-57
	LONG LEAD ITEMS	166	17-Feb-26 08:00	11-Jul-26 17:00	17-Feb-26 08:00 A	15-Sep-26 12:00 A	0.00	0.00	0.00	0%	0%	-57
	EXTERNAL / LANDSCAPE WORK	57	25-Feb-26 08:00	07-May-26 10:00	25-Feb-26 08:00 A	06-May-26 17:00 A	0.00	0.00	0.00	0%	0%	0
	SPORTS & RECREATIONAL FACILITIES WORK	124	17-Feb-26 08:00	05-Jul-26 17:00	17-Feb-26 08:00 A	02-Sep-26 17:00 A	0.00	0.00	0.00	0%	0%	-51
	CONCRETE WORK	41	07-Mar-26 08:00	28-Apr-26 10:00	07-Mar-26 08:00 A	27-Apr-26 17:00 A	0.00	0.00	0.00	0%	0%	0
	METAL WORK	45	11-Mar-26 08:00	07-May-26 10:00	11-Mar-26 08:00 A	06-May-26 17:00 A	0.00	0.00	0.00	0%	0%	0
	PLUMBING WORK	46	10-Mar-26 08:00	07-May-26 10:00	10-Mar-26 08:00 A	06-May-26 17:00 A	0.00	0.00	0.00	0%	0%	0
	IRRIGATION WORK	50	05-Mar-26 08:00	07-May-26 10:00	05-Mar-26 08:00 A	06-May-26 17:00 A	0.00	0.00	0.00	0%	0%	0
	ELECTRICAL WORK	100	11-May-26 08:00	11-Jul-26 17:00	11-May-26 08:00 A	15-Sep-26 12:00 A	0.00	0.00	0.00	0%	0%	-57
	SHORT LEAD ITEMS	28	17-Feb-26 08:00	28-Mar-26 10:00	17-Feb-26 08:00 A	26-Mar-26 17:00 A	0.00	0.00	0.00	0%	0%	0
	EXTERNAL / LANDSCAPE WORK	23	17-Feb-26 08:00	17-Mar-26 10:00	17-Feb-26 08:00 A	16-Mar-26 17:00 A	0.00	0.00	0.00	0%	0%	0
	CONCRETE WORK	28	17-Feb-26 08:00	28-Mar-26 10:00	17-Feb-26 08:00 A	26-Mar-26 17:00 A	0.00	0.00	0.00	0%	0%	0
	ARCHITECTURAL & FINISHES WORK	4	10-Mar-26 08:00	15-Mar-26 10:00	10-Mar-26 08:00 A	14-Mar-26 17:00 A	0.00	0.00	0.00	0%	0%	0
	METAL WORK	9	07-Mar-26 08:00	17-Mar-26 10:00	07-Mar-26 08:00 A	16-Mar-26 17:00 A	0.00	0.00	0.00	0%	0%	0
	HVAC WORK	19	23-Feb-26 08:00	17-Mar-26 10:00	23-Feb-26 08:00 A	16-Mar-26 17:00 A	0.00	0.00	0.00	0%	0%	0
	PLUMBING WORK	4	12-Mar-26 08:00	17-Mar-26 10:00	12-Mar-26 08:00 A	16-Mar-26 17:00 A	0.00	0.00	0.00	0%	0%	0
	IRRIGATION WORK	4	12-Mar-26 08:00	17-Mar-26 10:00	12-Mar-26 08:00 A	16-Mar-26 17:00 A	0.00	0.00	0.00	0%	0%	0
	ELECTRICAL WORK	4	12-Mar-26 08:00	17-Mar-26 10:00	12-Mar-26 08:00 A	16-Mar-26 17:00 A	0.00	0.00	0.00	0%	0%	0
	FIRE FIGHTING WORK	4	12-Mar-26 08:00	17-Mar-26 10:00	12-Mar-26 08:00 A	16-Mar-26 17:00 A	0.00	0.00	0.00	0%	0%	0
	MATERIAL APPROVALS	160	21-Feb-26 08:00	13-Jul-26 17:00	21-Feb-26 08:00 A	17-Sep-26 11:12 A	340,734.03	340,734.03	340,734.03	100%	100%	-56
	LONG LEAD ITEMS	157	25-Feb-26 08:00	13-Jul-26 17:00	25-Feb-26 08:00 A	17-Sep-26 11:12 A	284,659.98	284,659.98	284,659.98	100%	100%	-56
	EXTERNAL / LANDSCAPE WORK	56	25-Feb-26 08:00	05-May-26 17:00	25-Feb-26 08:00 A	05-May-26 17:00 A	15,425.28	15,425.28	15,425.28	100%	100%	0
	SPORTS & RECREATIONAL FACILITIES WORK	119	02-Mar-26 08:00	11-Jul-26 17:00	02-Mar-26 08:00 A	03-Sep-26 17:00 A	238,773.54	238,773.54	238,773.54	100%	100%	-47
	CONCRETE WORK	38	11-Mar-26 08:00	28-Apr-26 17:00	11-Mar-26 08:00 A	28-Apr-26 17:00 A	1,417.50	1,417.50	1,417.50	100%	100%	0
	METAL WORK	42	15-Mar-26 08:00	06-May-26 17:00	15-Mar-26 08:00 A	06-May-26 17:00 A	889.23	889.23	889.23	100%	100%	0
	PLUMBING WORK	42	15-Mar-26 08:00	06-May-26 17:00	15-Mar-26 08:00 A	06-May-26 17:00 A	3,553.95	3,553.95	3,553.95	100%	100%	0
	IRRIGATION WORK	45	11-Mar-26 08:00	06-May-26 17:00	11-Mar-26 08:00 A	06-May-26 17:00 A	6,802.65	6,802.65	6,802.65	100%	100%	0
	ELECTRICAL WORK	96	12-May-26 08:00	13-Jul-26 17:00	12-May-26 08:00 A	17-Sep-26 11:12 A	17,797.83	17,797.83	17,797.83	100%	100%	-56
	SHORT LEAD ITEMS	25	21-Feb-26 08:00	26-Mar-26 17:00	21-Feb-26 08:00 A	26-Mar-26 17:00 A	56,074.05	56,074.05	56,074.05	100%	100%	0

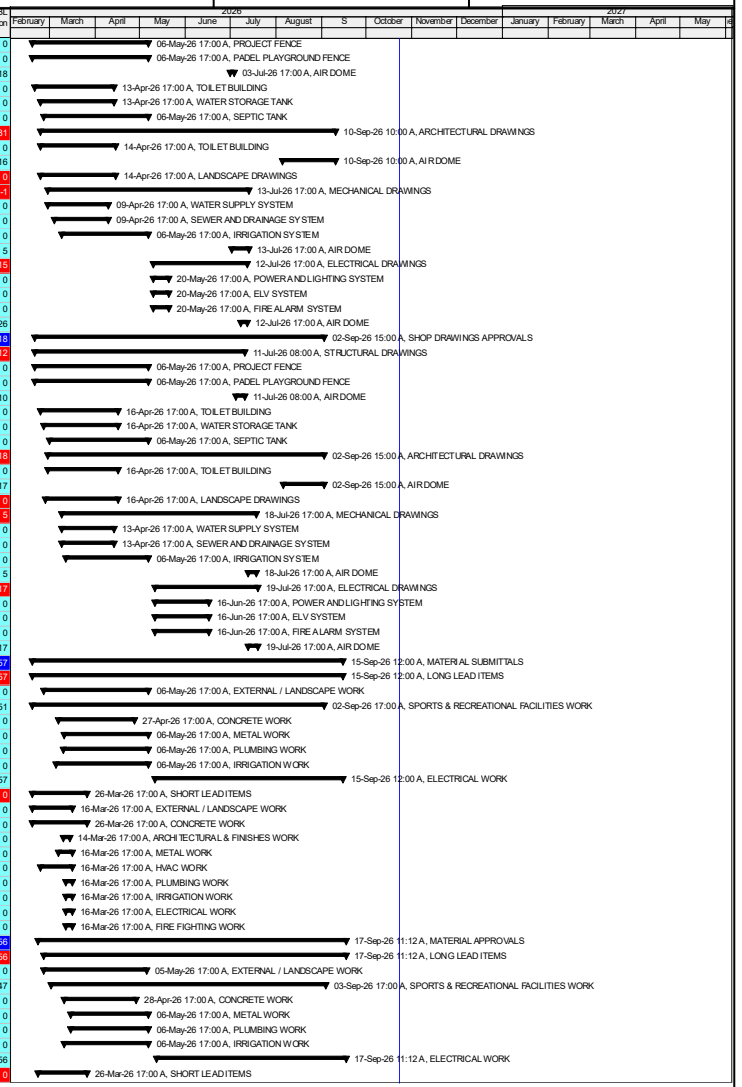


Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining W...
Milestone
summary

Baseline Schedule Rev.00

PLAYGROUNDS INITIATIVE - QASSIM, HAIL & TABUK - 25-Oct-2026

Activity ID	Activity Name	O.D	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Schedule % Complete	Performance % Complete	Variance - BL Project Duration
	EXTERNAL / LANDSCAPE WORK	25	21-Feb-26 08:00	26-Mar-26 17:00	21-Feb-26 08:00 A	26-Mar-26 17:00 A	38,542.29	38,542.29	38,542.29	100%	100%	0
	CONCRETE WORK	24	23-Feb-26 08:00	26-Mar-26 17:00	23-Feb-26 08:00 A	26-Mar-26 17:00 A	1,609.47	1,609.47	1,609.47	100%	100%	0
	ARCHITECTURAL & FINISHES WORK	2	15-Mar-26 08:00	16-Mar-26 17:00	15-Mar-26 08:00 A	16-Mar-26 17:00 A	7,931.55	7,931.55	7,931.55	100%	100%	0
	METAL WORK	10	11-Mar-26 08:00	26-Mar-26 17:00	11-Mar-26 08:00 A	26-Mar-26 17:00 A	478.89	478.89	478.89	100%	100%	0
	HVAC WORK	20	28-Feb-26 08:00	26-Mar-26 17:00	28-Feb-26 08:00 A	26-Mar-26 17:00 A	606.36	606.36	606.36	100%	100%	0
	PLUMBING WORK	2	25-Mar-26 08:00	26-Mar-26 17:00	25-Mar-26 08:00 A	26-Mar-26 17:00 A	3,147.03	3,147.03	3,147.03	100%	100%	0
	IRRIGATION WORK	2	25-Mar-26 08:00	26-Mar-26 17:00	25-Mar-26 08:00 A	26-Mar-26 17:00 A	3,328.23	3,328.23	3,328.23	100%	100%	0
	ELECTRICAL WORK	2	25-Mar-26 08:00	26-Mar-26 17:00	25-Mar-26 08:00 A	26-Mar-26 17:00 A	407.52	407.52	407.52	100%	100%	0
	FIRE FIGHTING WORK	2	25-Mar-26 08:00	26-Mar-26 17:00	25-Mar-26 08:00 A	26-Mar-26 17:00 A	22.71	22.71	22.71	100%	100%	0
	PROCUREMENT	201	26-Feb-26 08:00	27-Aug-26 17:00	26-Feb-26 08:00 A	27-Oct-26 12:48	3,066,606.27	2,662,883.45	3,066,606.27	100%	86.83%	-51
	LONG LEAD ITEMS	194	07-Mar-26 08:00	27-Aug-26 17:00	07-Mar-26 08:00 A	27-Oct-26 12:48	2,561,939.82	2,161,684.91	2,561,939.82	100%	84.38%	-51
	PURCHASE ORDER	157	07-Mar-26 08:00	16-Jul-26 17:00	07-Mar-26 08:00 A	10-Sep-26 17:00 A	0.00	0.00	0.00	0%	0%	-48
	EXTERNAL / LANDSCAPE WORK	49	07-Mar-26 08:00	07-May-26 10:00	07-Mar-26 08:00 A	06-May-26 17:00 A	0.00	0.00	0.00	0%	0%	0
	SPORTS & RECREATIONAL FACILITIES WORK	119	26-Mar-26 08:00	16-Jul-26 17:00	26-Mar-26 08:00 A	10-Sep-26 17:00 A	0.00	0.00	0.00	0%	0%	-48
	CONCRETE WORK	39	18-Mar-26 08:00	07-May-26 10:00	18-Mar-26 08:00 A	06-May-26 17:00 A	0.00	0.00	0.00	0%	0%	0
	METAL WORK	38	24-Mar-26 08:00	07-May-26 10:00	24-Mar-26 08:00 A	06-May-26 17:00 A	0.00	0.00	0.00	0%	0%	0
	PLUMBING WORK	35	28-Mar-26 08:00	07-May-26 10:00	28-Mar-26 08:00 A	06-May-26 17:00 A	0.00	0.00	0.00	0%	0%	0
	IRRIGATION WORK	40	17-Mar-26 08:00	07-May-26 10:00	17-Mar-26 08:00 A	06-May-26 17:00 A	0.00	0.00	0.00	0%	0%	0
	ELECTRICAL WORK	105	11-May-26 08:00	16-Jul-26 17:00	11-May-26 08:00 A	10-Sep-26 09:36 A	0.00	0.00	0.00	0%	0%	-47
	MANUFACTURE / FABRICATION	140	29-Apr-26 08:00	16-Aug-26 17:00	29-Apr-26 08:00 A	15-Oct-26 17:00 A	0.00	0.00	0.00	0%	0%	-51
	EXTERNAL / LANDSCAPE WORK	102	06-May-26 08:00	23-Jul-26 17:00	06-May-26 08:00 A	10-Sep-26 17:00 A	0.00	0.00	0.00	0%	0%	-42
	SPORTS & RECREATIONAL FACILITIES WORK	124	06-May-26 08:00	16-Aug-26 17:00	06-May-26 08:00 A	15-Oct-26 17:00 A	0.00	0.00	0.00	0%	0%	-51
	CONCRETE WORK	64	29-Apr-26 08:00	30-Jun-26 17:00	29-Apr-26 08:00 A	02-Jul-26 17:00 A	0.00	0.00	0.00	0%	0%	-2
	METAL WORK	119	06-May-26 08:00	23-Jul-26 17:00	06-May-26 08:00 A	27-Sep-26 17:00 A	0.00	0.00	0.00	0%	0%	-55
	PLUMBING WORK	102	06-May-26 08:00	23-Jul-26 17:00	06-May-26 08:00 A	14-Sep-26 17:00 A	0.00	0.00	0.00	0%	0%	-45
	IRRIGATION WORK	99	06-May-26 08:00	30-Jun-26 17:00	06-May-26 08:00 A	21-Sep-26 12:24 A	0.00	0.00	0.00	0%	0%	-71
	ELECTRICAL WORK	129	12-May-26 08:00	10-Aug-26 17:00	12-May-26 08:00 A	30-Sep-26 17:00 A	0.00	0.00	0.00	0%	0%	-43
	DELIVERY TO SITE	146	06-May-26 08:00	27-Aug-26 17:00	06-May-26 08:00 A	27-Oct-26 12:48	2,561,939.82	2,161,684.91	2,561,939.82	100%	84.38%	-51
	EXTERNAL / LANDSCAPE WORK	114	06-May-26 08:00	06-Aug-26 17:00	06-May-26 08:00 A	25-Oct-26 09:36	138,827.52	137,434.65	138,827.52	100%	99%	-66
	SPORTS & RECREATIONAL FACILITIES WORK	129	06-May-26 08:00	27-Aug-26 17:00	06-May-26 08:00 A	25-Oct-26 17:00	2,148,961.86	1,759,714.44	2,148,961.86	100%	81.89%	-49
	CONCRETE WORK	63	06-May-26 08:00	06-Jul-26 17:00	06-May-26 08:00 A	05-Jul-26 17:00 A	12,757.50	12,757.50	12,757.50	100%	100%	1
	METAL WORK	131	06-May-26 08:00	06-Aug-26 17:00	06-May-26 08:00 A	27-Oct-26 12:48	8,003.07	6,974.78	8,003.07	100%	87.15%	-69
	PLUMBING WORK	108	06-May-26 08:00	06-Aug-26 17:00	06-May-26 08:00 A	15-Oct-26 17:00 A	31,985.55	31,985.55	31,985.55	100%	100%	-59
	IRRIGATION WORK	98	06-May-26 08:00	05-Jul-26 17:00	06-May-26 08:00 A	24-Oct-26 11:12	61,223.85	59,587.38	61,223.85	100%	97.33%	-93
	ELECTRICAL WORK	140	13-May-26 08:00	24-Aug-26 17:00	13-May-26 08:00 A	25-Oct-26 15:24	160,180.47	153,230.61	160,180.47	100%	95.66%	-52
	SHORT LEAD ITEMS	190	26-Feb-26 08:00	22-Jul-26 17:00	26-Feb-26 08:00 A	25-Oct-26 09:36	504,666.45	500,998.54	504,666.45	100%	99.27%	-79
	PURCHASE ORDER	163	26-Feb-26 08:00	11-Jul-26 17:00	26-Feb-26 08:00 A	27-Aug-26 17:00 A	0.00	0.00	0.00	0%	0%	-41
	EXTERNAL / LANDSCAPE WORK	163	26-Feb-26 08:00	11-Jul-26 17:00	26-Feb-26 08:00 A	27-Aug-26 17:00 A	0.00	0.00	0.00	0%	0%	-41
	CONCRETE WORK	41	02-Mar-26 08:00	23-Apr-26 10:00	02-Mar-26 08:00 A	22-Apr-26 17:00 A	0.00	0.00	0.00	0%	0%	0
	ARCHITECTURAL & FINISHES WORK	7	05-May-26 08:00	13-May-26 10:00	05-May-26 08:00 A	12-May-26 17:00 A	0.00	0.00	0.00	0%	0%	0
	METAL WORK	7	05-May-26 08:00	13-May-26 10:00	05-May-26 08:00 A	12-May-26 17:00 A	0.00	0.00	0.00	0%	0%	0
	HVAC WORK	7	05-May-26 08:00	13-May-26 10:00	05-May-26 08:00 A	12-May-26 17:00 A	0.00	0.00	0.00	0%	0%	0
	PLUMBING WORK	7	05-May-26 08:00	13-May-26 10:00	05-May-26 08:00 A	12-May-26 17:00 A	0.00	0.00	0.00	0%	0%	0
	IRRIGATION WORK	7	05-May-26 08:00	13-May-26 10:00	05-May-26 08:00 A	12-May-26 17:00 A	0.00	0.00	0.00	0%	0%	0
	ELECTRICAL WORK	97	11-May-26 08:00	02-Jul-26 17:00	11-May-26 08:00 A	27-Aug-26 17:00 A	0.00	0.00	0.00	0%	0%	-48
	FIRE FIGHTING WORK	94	11-May-26 08:00	29-Jun-26 17:00	11-May-26 08:00 A	27-Aug-26 17:00 A	0.00	0.00	0.00	0%	0%	-51
	DELIVERY TO SITE	188	01-Mar-26 08:00	22-Jul-26 17:00	01-Mar-26 08:00 A	25-Oct-26 09:36	504,666.45	500,998.54	504,666.45	100%	99.27%	-79
	EXTERNAL / LANDSCAPE WORK	171	01-Mar-26 08:00	22-Jul-26 17:00	01-Mar-26 08:00 A	24-Oct-26 17:00	346,880.61	344,882.80	346,880.61	100%	99.42%	-79
	CONCRETE WORK	52	10-Mar-26 08:00	13-May-26 17:00	10-Mar-26 08:00 A	13-May-26 17:00 A	14,485.23	14,485.23	14,485.23	100%	100%	0
	ARCHITECTURAL & FINISHES WORK	7	06-May-26 08:00	13-May-26 17:00	06-May-26 08:00 A	13-May-26 17:00 A	71,383.95	71,383.95	71,383.95	100%	100%	0
	METAL WORK	135	06-May-26 08:00	08-Jul-26 17:00	06-May-26 08:00 A	25-Oct-26 09:36	4,310.01	4,137.61	4,310.01	100%	96%	-91
	HVAC WORK	7	06-May-26 08:00	13-May-26 17:00	06-May-26 08:00 A	13-May-26 17:00 A	5,457.24	5,457.24	5,457.24	100%	100%	0
	PLUMBING WORK	7	06-May-26 08:00	13-May-26 17:00	06-May-26 08:00 A	13-May-26 17:00 A	28,323.27	28,323.27	28,323.27	100%	100%	0
	IRRIGATION WORK	97	06-May-26 08:00	05-Jul-26 17:00	06-May-26 08:00 A	24-Oct-26 15:48	29,954.07	28,456.37	29,954.07	100%	95%	-94
	ELECTRICAL WORK	118	13-May-26 08:00	16-Jul-26 17:00	13-May-26 08:00 A	15-Oct-26 17:00 A	3,667.68	3,667.68	3,667.68	100%	100%	-77
	FIRE FIGHTING WORK	126	13-May-26 08:00	09-Jul-26 17:00	13-May-26 08:00 A	15-Oct-26 17:00 A	204.39	204.39	204.39	100%	100%	-83
	CONSTRUCTION STAGE	263	24-Mar-26 08:00	14-Dec-26 17:00	24-Mar-26 08:00 A	30-Jan-27 17:00	5,438,906.71	3,588,645.67	6,814,680.60	79.81%	52.66%	-40
	PLAYGROUND AND LANDSCAPING WORKS	246	24-Mar-26 08:00	14-Dec-26 17:00	24-Mar-26 08:00 A	10-Jan-27 16:12	2,013,546.81	2,072,784.96	2,311,795.02	87.1%	89.66%	-23
	CUT AND FILL	38	24-Mar-26 08:00	06-May-26 17:00	24-Mar-26 08:00 A	06-May-26 17:00 A	228,240.00	228,240.00	228,240.00	100%	100%	0
	PLAYGROUND WORKS	186	23-Apr-26 08:00	07-Dec-26 17:00	23-Apr-26 08:00 A	03-Dec-26 15:00	550,592.94	537,405.24	623,491.20	88.31%	86.19%	3
	FOOTBALL PLAYGROUND WORKS	170	23-Apr-26 08:00	17-Nov-26 17:00	23-Apr-26 08:00 A	12-Nov-26 16:12	307,563.00	297,308.33	333,290.16	92.28%	89.2%	4
	BASKETBALL PLAYGROUND WORKS	163	06-May-26 08:00	17-Nov-26 17:00	06-May-26 08:00 A	19-Nov-26 09:36	167,045.38	157,108.46	173,211.12	96.44%	90.7%	-1
	PADEL PLAYGROUND WORKS	175	06-May-26 08:00	07-Dec-26 17:00	06-May-26 08:00 A	03-Dec-26 15:00	75,984.56	82,988.45	116,989.92	64.95%	70.94%	3
	GENERAL SITE WORKS	226	16-Apr-26 08:00	14-Dec-26 17:00	16-Apr-26 08:00 A	10-Jan-27 16:12	594,275.82	536,348.31	656,604.42	90.51%	81.69%	-23
	FENCE WORKS	160	16-Apr-26 08:00	17-Aug-26 17:00	16-Apr-26 08:00 A	15-Oct-26 17:00 A	32,909.40	32,909.40	32,909.40	100%	100%	-50
	MECHANICAL WORK	154	12-May-26 08:00	10-Aug-26 17:00	12-May-26 08:00 A	14-Nov-26 10:24	230,187.54	201,030.97	230,187.54	100%	87.33%	-80
	STORM WATER AND UTILITY WORK	149	12-May-26 08:00	04-Aug-26 17:00	12-May-26 08:00 A	08-Nov-26 10:24	27,252.00	16,806.00	27,252.00	100%	61.67%	-80
	IRRIGATION SYSTEM WORKS	96	02-Jun-26 08:00	30-Jul-26 17:00	02-Jun-26 08:00 A	03-Nov-26 10:24	202,617.60	184,224.97	202,617.60	100%	90.92%	-80
	FIRE PROTECTION SYSTEM	5	05-Aug-26 08:00	10-Aug-26 17:00	08-Nov-26 10:24	14-Nov-26 10:24	317.94	0.00	317.94	100%	0%	0
	ELECTRICAL WORK	180	08-Jun-26 08:00	07-Nov-26 17:00	08-Jun-26 08:00 A	20-Dec-26 16:12	324,720.48	272,439.15	345,859.68	93.89%	78.77%	-37
	POWER, LIGHTING & GROUNDING	147	08-Jun-26 08:00	27-Sep-26 17:00	08-Jun-26 08:00 A	26-Nov-26 12:00	288,789.48	240,981.87	288,789.48	100%	83.45%	-52

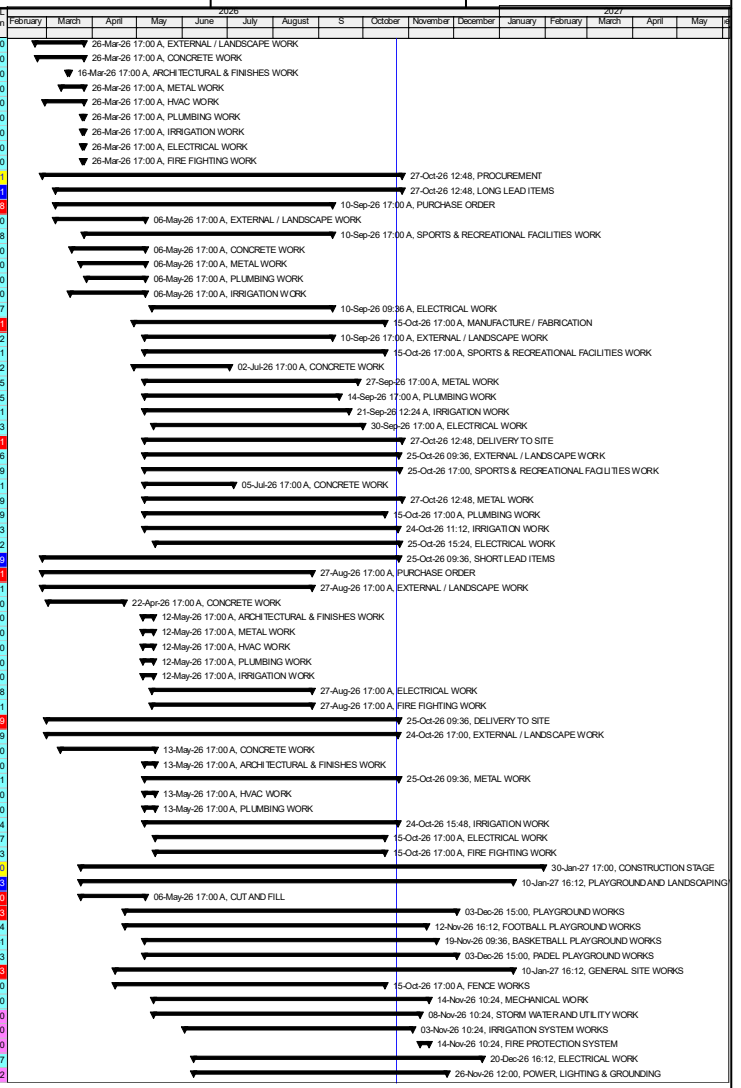


Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining W...
Milestone
summary

Baseline Schedule Rev.00

PLAYGROUNDS INITIATIVE - QASSIM, HAIL & TABUK - 25-Oct-2026

Activity ID	Activity Name	O.D	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Schedule % Complete	Performance % Complete	Variance - BL Project Duration
	ELV SYSTEMS (TELECOM, DATA, AV & CCTV)	25	28-Sep-26 08:00	26-Oct-26 17:00	22-Sep-26 08:48 A	08-Dec-26 12:00	28,266.00	25,887.60	43,146.00	65.51%	60%	-40
	FIRE ALARM SYSTEM	32	01-Oct-26 08:00	07-Nov-26 17:00	13-Oct-26 08:00 A	20-Dec-26 16:12	7,665.00	5,569.68	13,924.20	55.05%	40%	-27
	PARKING WORK	161	17-Jun-26 08:00	11-Nov-26 17:00	17-Jun-26 08:00 A	20-Dec-26 16:12	5,788.80	25,728.00	40,207.80	14.4%	63.99%	-33
	SERVICE CONNECTION	183	10-Jun-26 08:00	14-Dec-26 17:00	10-Jun-26 08:00 A	10-Jan-27 16:12	669.60	4,240.80	7,440.00	9%	57%	-23
	LANDSCAPING WORKS	156	31-May-26 08:00	22-Nov-26 17:00	30-May-26 16:12 A	10-Nov-26 14:36	592,147.65	733,167.09	755,169.00	78.41%	97.09%	10
	HARDSCAPE WORK	156	31-May-26 08:00	22-Nov-26 17:00	30-May-26 16:12 A	10-Nov-26 14:36	521,665.65	634,411.29	648,147.00	80.49%	97.88%	10
	SOFTSCAPE WORK	143	10-Jun-26 08:00	22-Nov-26 17:00	10-Jun-26 08:00 A	10-Nov-26 14:36	70,482.00	98,755.80	107,022.00	65.86%	92.28%	10
	TANK WORKS	150	13-May-26 08:00	27-Sep-26 17:00	13-May-26 08:00 A	03-Nov-26 12:00	48,290.40	37,624.32	48,290.40	100%	77.91%	-32
	SEPTIC TANK	146	13-May-26 08:00	03-Sep-26 17:00	13-May-26 08:00 A	01-Nov-26 17:00	7,475.22	7,223.04	7,475.22	100%	96.63%	-49
	WATER STORAGE TANK	150	13-May-26 08:00	27-Sep-26 17:00	13-May-26 08:00 A	03-Nov-26 12:00	40,815.18	30,401.28	40,815.18	100%	74.49%	-32
	AIR DOME CONSTRUCTION	220	13-May-26 08:00	03-Dec-26 17:00	13-May-26 08:00 A	30-Jan-27 17:00	3,110,229.58	1,210,693.39	4,178,041.20	74.44%	28.98%	-49
	CIVIL WORK	152	13-May-26 08:00	14-Sep-26 17:00	13-May-26 08:00 A	11-Nov-26 17:00	1,711,669.97	1,210,693.39	1,711,669.97	100%	70.73%	-49
	ARCHITECTURAL WORK	25	05-Nov-26 08:00	03-Dec-26 17:00	02-Jan-27 08:00	30-Jan-27 17:00	0.00	0.00	712,953.22	0%	0%	0
	MECHANICAL WORK	23	15-Sep-26 08:00	12-Oct-26 17:00	12-Nov-26 08:00	08-Dec-26 17:00	667,968.77	0.00	667,968.77	100%	0%	0
	ELECTRICAL WORK	33	28-Sep-26 08:00	04-Nov-26 17:00	24-Nov-26 08:00	31-Dec-26 17:00	730,590.84	0.00	1,085,449.25	67.31%	0%	0
	TOILET BUILDING WORKS	143	12-May-26 08:00	28-Oct-26 17:00	12-May-26 08:00 A	28-Oct-26 11:12	315,130.32	305,167.32	324,844.38	97.01%	93.94%	1
	CIVIL WORK	143	12-May-26 08:00	26-Oct-26 17:00	12-May-26 08:00 A	27-Oct-26 12:48	217,539.78	221,677.98	227,117.58	95.78%	97.6%	-1
	STRUCTURAL WORK	59	12-May-26 08:00	01-Aug-26 17:00	12-May-26 08:00 A	12-Aug-26 17:00 A	37,980.00	37,980.00	37,980.00	100%	100%	-10
	ARCHITECTURAL WORK	76	02-Aug-26 08:00	26-Oct-26 17:00	01-Aug-26 08:00 A	27-Oct-26 12:48	179,559.78	183,697.98	189,137.58	94.94%	97.12%	-2
	GENERAL FINISHES	76	02-Aug-26 08:00	21-Oct-26 17:00	01-Aug-26 08:00 A	07-Sep-26 09:36 A	84,120.00	84,120.00	84,120.00	100%	100%	37
	WET AREA FINISHES	37	26-Aug-26 08:00	13-Oct-26 17:00	06-Aug-26 08:00 A	26-Oct-26 08:48	81,123.78	79,515.30	81,123.78	100%	98.02%	-27
	ROOF FINISHES	46	07-Oct-26 08:00	26-Oct-26 17:00	14-Aug-26 08:00 A	27-Oct-26 12:48	14,316.00	20,062.68	23,893.80	59.92%	83.97%	-46
	MEP WORK	103	16-Jun-26 08:00	28-Oct-26 17:00	16-Jun-26 08:00 A	28-Oct-26 11:12	97,590.54	83,489.34	97,726.80	99.86%	85.43%	1
	MECANICAL WORKS	103	16-Jun-26 08:00	28-Oct-26 17:00	16-Jun-26 08:00 A	28-Oct-26 11:12	79,343.22	65,242.02	79,479.48	99.83%	82.09%	1
	FIRE FIGHTING SYSTEM	2	27-Oct-26 08:00	28-Oct-26 17:00	23-Sep-26 11:12 A	28-Oct-26 11:12	0.00	81.76	136.26	0%	60%	-27
	SEWER AND DRAINAGE SYSTEM	92	16-Jun-26 08:00	05-Sep-26 17:00	16-Jun-26 08:00 A	25-Oct-26 12:00	11,290.02	10,322.30	11,290.02	100%	91.43%	-42
	HVAC SYSTEM	42	09-Aug-26 08:00	12-Oct-26 17:00	13-Aug-26 08:00 A	26-Oct-26 08:48	12,127.20	9,821.76	12,127.20	100%	80.99%	-7
	WATER SUPPLY SYSTEM	45	12-Aug-26 08:00	02-Sep-26 17:00	22-Jul-26 08:00 A	24-Oct-26 16:12	55,926.00	45,016.20	55,926.00	100%	80.49%	-61
	ELECTRICAL WORKS	38	15-Aug-26 08:00	17-Sep-26 17:00	22-Jul-26 08:00 A	16-Sep-26 10:24 A	18,247.32	18,247.32	18,247.32	100%	100%	-18
	PROJECT CLOSOUT	221	25-May-26 08:00	16-Dec-26 17:00	25-May-26 08:00 A	11-Feb-27 17:00	34,073.40	210,119.32	1,135,780.10	3%	18.5%	-49

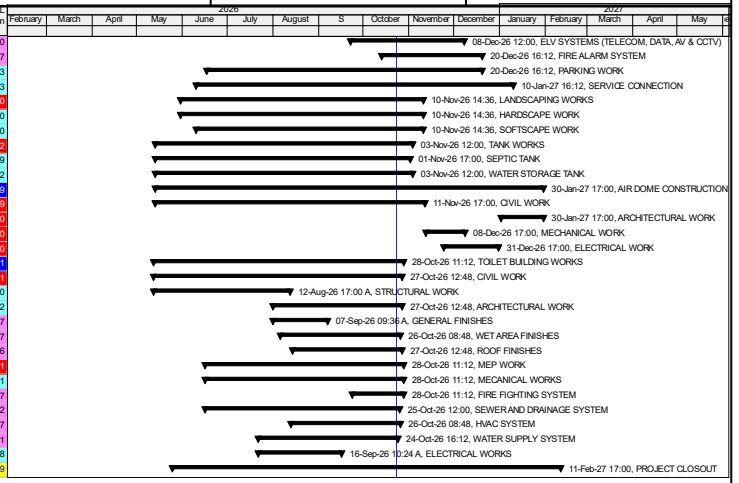

Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining W...
Milestone
summary

Baseline Schedule Rev.00
