
Infrastructure Works of Area J -3rd Industrial City-Dammam-Phase 2 - Update 13-10-2026

WBS Summary Schedule

Activity ID	Activity Name	Original Duration	BL Project Start	BL Project Finish	Start	Finish	Performance % Complete
Infrastructure Works of Area J -3rd Industrial City-Dammam-Pha		892	12-Jan-25	11-Jan-27	12-Jan-25 A	20-Dec-27	75.01%
Key Milestones		892	12-Jan-25	11-Jan-27	12-Jan-25 A	20-Dec-27	0%
Preliminaries and Mobilization Works		48	12-Jan-25	09-Mar-25	12-Jan-25 A	12-Mar-25 A	0%
Engineering Works		31	12-Jan-25	16-Feb-25	12-Jan-25 A	02-Jun-25 A	100%
Procurement Cycle		749	05-Feb-25	05-Oct-26	11-Feb-25 A	29-Jul-27	87.55%
Construction Works		856	09-Feb-25	28-Dec-26	11-Feb-25 A	06-Dec-27	72.51%
Testing and Comissioning		278	25-Aug-26	03-Jan-27	01-Jun-26 A	06-Dec-27	64.59%
Handing over and close out		160	17-Oct-26	11-Jan-27	16-Jun-27	20-Dec-27	0%

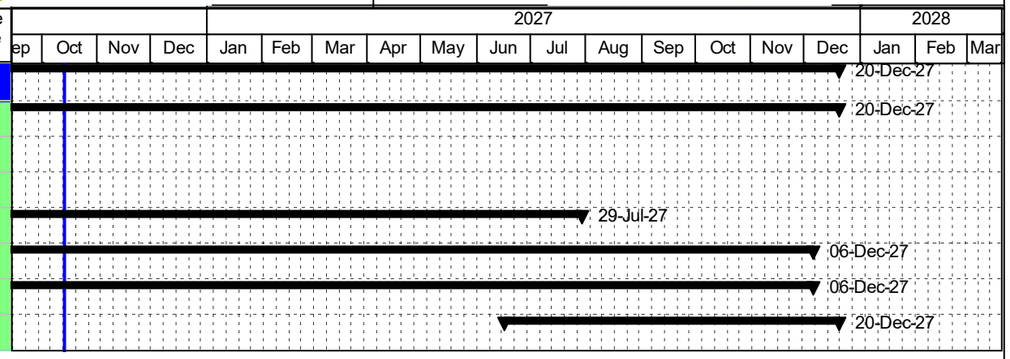

Primary Baseline
Remaining Work
Critical Remaining Work
Actual Work
Baseline Milestone
Milestone
Summary

Date	Revision	Checked	Approved
13-Oct-26	Third Industrial City		
