Ready-Built Factories Program, Package 3: 20 Factories of 900 m² in Hail

برنامج المصانع الجاهزة و المنتجات الجديدة الحزمة الثالثة (المحفظة الاستثمارية) - حائل 20 مصنع 900 متر

CLIENT	WEEKLY REPORT	PROJECT START	CONTRACT COMPLETION	P6 FORECAST FINISH	SCHEDULE ACTIVITIES
MODON	No. 41	04-Dec-2025	03-Dec-2026	02-Nov-2026	1,827

Scope: 20 ready-built factories of 900 m² each in five blocks (A to E), with site works, networks, external works, roads and landscaping.

Status at a glance

Progress is measured as physical % complete, weighted by budgeted man-hours. At the 19-Oct-2026 data date the project is 97.2% complete against 96.5% planned, 0.7% ahead. Engineering, procurement and mobilisation are complete, construction is on plan at 96.4%, and testing and commissioning is ahead of plan.

PHYSICAL % COMPLETE
97.2% / 96.5% plan
▲ SPI 1.01 +0.7%

PROGRESS THIS WEEK
—
Not stated in the files of this upload.

CONTRACT TIME ELAPSED
87.6% · day 319 of 364
▲ P6 finish 02-Nov-2026

SCHEDULE ACTIVITIES COMPLETED
93.1% · 1,701 of 1,827
60 in progress, 66 not started

The forecast finish is 31 days early, but with zero float.

The P6 update finishes the project on 02-Nov-2026, 31 days before the contract completion date of 03-Dec-2026. Project completion, construction finish and external works all have zero float. Road works are 68.8% complete with curb stones, interlock tiles and road signs still at 0%, and fences and gates are at 67.1% against 90.0% planned.

Site photos this week

Four photos from the weekly report workbook No. 41, camera-stamped 18-Oct-2026. Asphalt is being laid on the internal roads beside the finished factory buildings. Select a photo to view it larger, then use the arrows to move between photos.



Factory building front
Cladding, roller shutter and glazed office front in place. Stamped 18-Oct-2026, 07:04.



Internal road asphalt
New asphalt layer with a roller working ahead. Stamped 18-Oct-2026, 08:05.



Asphalt paving

Paver and crew on the road beside the factory row. Stamped 18-Oct-2026, 08:39.



Road works

One lane asphalted, the second still on base course. Stamped 18-Oct-2026, 08:41.

Progress by phase


Physical progress to date by WBS, weighted by budgeted man-hours (P6 labour units).
Source: P6 update report No. 41, data date 19-Oct-2026.

PHASE	WEIGHT	PLANNED	ACTUAL	VARIANCE	SPI	STATUS
Mobilisation	0.8%	100.0%	100.0%	0.0	1.00	✓ Complete
Engineering	12.6%	100.0%	100.0%	0.0	1.00	✓ Complete
Procurement	23.5%	100.1%	100.1%	0.0	1.00	✓ Complete
Construction	59.1%	96.4%	96.4%	0.0	1.00	▲ On track
Testing & commissioning	3.4%	74.0%	92.9%	+18.9	1.26	▲ Ahead
Project close-out and demobilisation	0.5%	0.0%	0.0%	0.0	–	● Starts 19-Oct-2026
Total	100%	**96.5%**	**97.2%**	**+0.7**	**1.01**	▲ On track

Weights are each phase's share of the 116,740 budgeted man-hours. The schedule's own WBS labels give different weights (engineering 3%, procurement 27%, construction 60%, testing and commissioning 10%). The P6 update has 1,827 activities: 1,701 completed, 60 in progress and 66 not started.

Scope of work: factory blocks

Budgeted and earned man-hours for each factory block and for the site infrastructure, by discipline, from the P6 update report No. 41. No quantity tables were uploaded this week, and the files hold no previous-week figures, so the "This week" column shows "–".

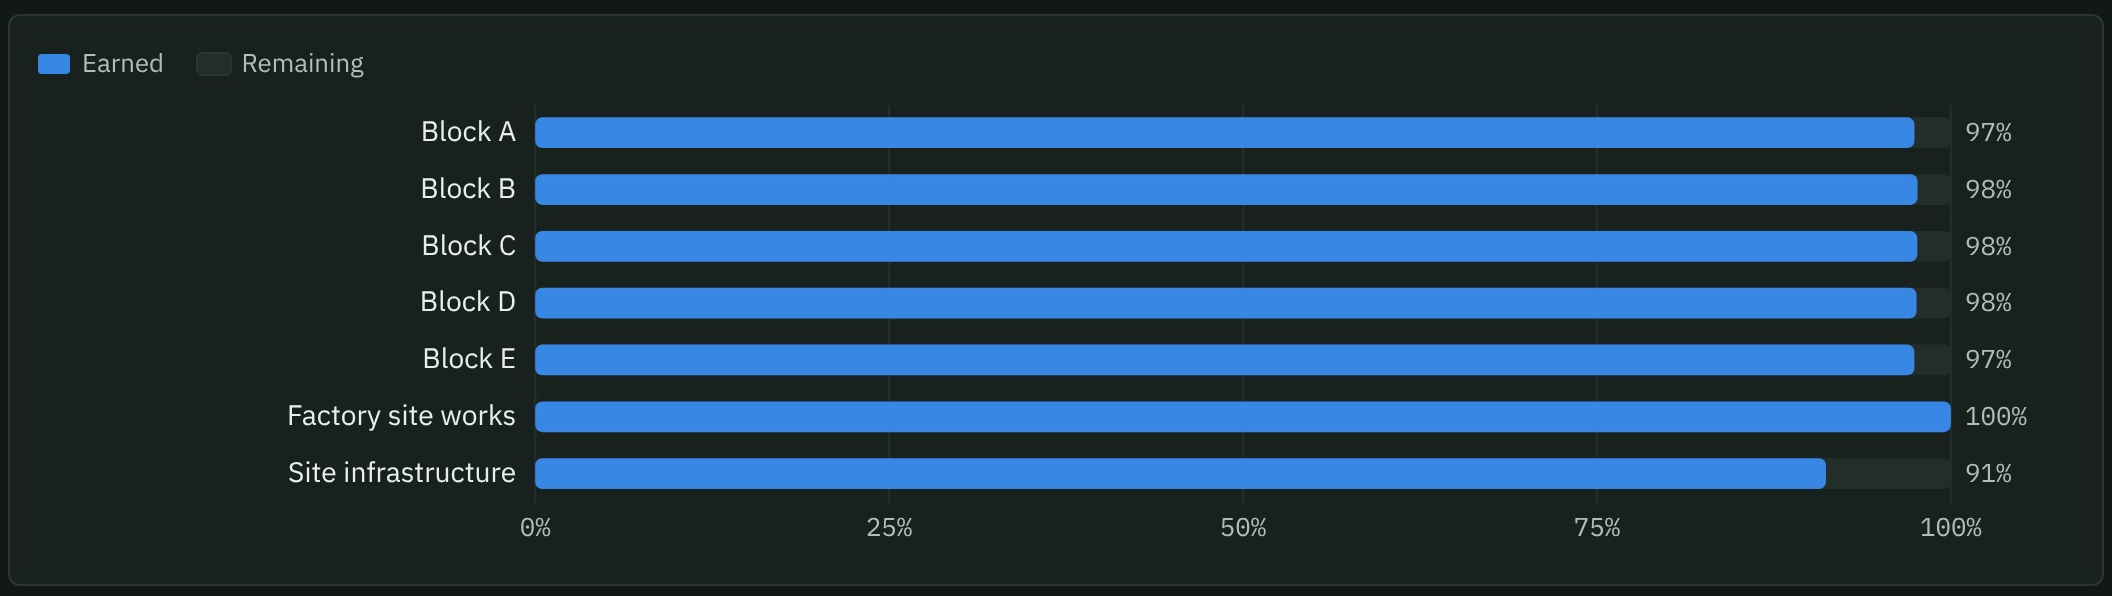

SCOPE ITEM	DISCIPLINE	UNIT	BUDGETED	EARNED	THIS WEEK	REMAINING	% COMPLETE
Block A	Structural	MH	3,008	3,008	–	0	100.0%
	Structural steel	MH	2,512	2,512	–	0	100.0%
	Architectural	MH	2,928	2,709	–	219	92.5%
	Mechanical	MH	1,088	1,088	–	0	100.0%
	Electrical	MH	1,264	1,205	–	59	95.3%
	Total	MH	**10,800**	**10,522**	**–**	**278**	**97.4%**
Block B	Structural	MH	3,072	3,072	–	0	100.0%
	Structural steel	MH	2,512	2,512	–	0	100.0%
	Architectural	MH	2,992	2,773	–	219	92.7%
	Mechanical	MH	1,088	1,088	–	0	100.0%
	Electrical	MH	1,248	1,210	–	38	97.0%
	Total	MH	**10,912**	**10,655**	**–**	**257**	**97.6%**
Block C	Structural	MH	2,960	2,960	–	0	100.0%
	Structural steel	MH	2,512	2,512	–	0	100.0%
	Architectural	MH	2,896	2,677	–	219	92.4%
	Mechanical	MH	1,088	1,088	–	0	100.0%
	Electrical	MH	1,248	1,213	–	35	97.2%
	Total	MH	**10,704**	**10,450**	**–**	**254**	**97.6%**
Block D	Structural	MH	3,008	3,008	–	0	100.0%
	Structural steel	MH	2,512	2,512	–	0	100.0%
	Architectural	MH	2,928	2,709	–	219	92.5%
	Mechanical	MH	1,088	1,088	–	0	100.0%
	Electrical	MH	1,264	1,221	–	43	96.6%
	Total	MH	**10,800**	**10,538**	**–**	**262**	**97.6%**
Block E	Structural	MH	3,040	3,040	–	0	100.0%
	Structural steel	MH	2,512	2,512	–	0	100.0%
	Architectural	MH	2,896	2,677	–	219	92.4%

SCOPE ITEM	DISCIPLINE	UNIT	BUDGETED	EARNED	THIS WEEK	REMAINING	% COMPLETE
	Mechanical	MH	1,088	1,088	–	0	100.0%
	Electrical	MH	1,280	1,220	–	60	95.3%
	Total	MH	**10,816**	**10,537**	–	**279**	**97.4%**
Factory site works	All	MH	1,808	1,808	–	0	100.0%
Site infrastructure	Site works	MH	1,376	1,376	–	0	100.0%
	Networks	MH	4,960	4,960	–	0	100.0%
	External works: mechanical	MH	2,384	2,384	–	0	100.0%
	External works: electrical	MH	624	584	–	40	93.6%
	External electrical works	MH	1,136	1,008	–	128	88.7%
	Fences and gates	MH	1,360	912	–	448	67.1%
	Road works	MH	1,136	782	–	354	68.8%
	Landscaping	MH	192	0	–	192	0.0%
	Total	MH	**13,168**	**12,006**	–	**1,162**	**91.2%**

Architectural finishes in every block

Structure, structural steel and mechanical works are complete in all five blocks. Architectural works stand at 92.4–92.7% against 100% planned: metal works (steel railings) are at 69.2% in each block and specialties (furniture, identification signs) at 50.0–58.3%. Electrical works are at 95.3–97.2%.

Site infrastructure: 91.2%

Site works and all networks are complete. Fences and gates are at 67.1% against 90.0% planned and external electrical works at 88.7% against 100%. Road works are at 68.8%, on plan, and landscaping (trees and shrubs) is due to start on 21-Oct-2026.

Milestones

Baseline dates and P6 forecasts from the P6 update report No. 41, with total float from the P6 update (XER) file. The weekly report workbook has no text version, so its own forecasts could not be compared.

MILESTONE	BASELINE	P6 UPDATE FORECAST	CHANGE (DAYS)	P6 FLOAT (DAYS)	STATUS
Project start	04-Dec-2025	04-Dec-2025 (actual)	0	–	✓ Done
Construction start	24-Dec-2025	28-Dec-2025 (actual)	+4	–	✓ Done
Complete mobilisation	04-Jan-2026	05-Jan-2026 (actual)	+1	–	✓ Done
Site levelling, local roads and parking	07-Jan-2026	05-Jan-2026 (actual)	−2	–	✓ Done
Network start	03-Jun-2026	05-May-2026 (actual)	−29	–	✓ Done
Engineering and materials complete	09-Apr-2026	19-Oct-2026	+193	2.8	▼ Late
Civil works complete	14-Jul-2026	19-Oct-2026	+97	5.8	▼ Late
Environmental works complete	11-Oct-2026	19-Oct-2026	+8	10.8	▼ Late
Testing and commissioning complete	25-Oct-2026	21-Oct-2026	−4	10.1	● On time
Mechanical works complete	01-Oct-2026	24-Oct-2026	+23	6.5	▼ Late
Architectural works complete	04-Oct-2026	27-Oct-2026	+23	2.8	▼ Late
Electrical works complete	26-Nov-2026	27-Oct-2026	−30	2.8	● On time
Construction complete	09-Nov-2026	31-Oct-2026	−9	2.0	● On time
External works complete	09-Nov-2026	31-Oct-2026	−9	0	● Zero float

MILESTONE	BASELINE	P6 UPDATE FORECAST	CHANGE (DAYS)	P6 FLOAT (DAYS)	STATUS
Project completion	03-Dec-2026	02-Nov-2026	−31	0	Zero float

Interim milestones are late against the baseline, but completion is forecast early.

Civil, mechanical and architectural completion are 23 to 97 days behind their baseline dates, yet construction and project completion are forecast 9 and 31 days early. Completion, construction finish and external works have no float left, so any slip in road works, fences and gates or the handover activities moves the finish date.

Procurement of key materials

Share of budgeted procurement man-hours earned for each material package. Source: P6 update report No. 41.



All material packages are delivered.

Every long-lead and short-lead package has an actual finish for delivery to site. The last packages, external works materials, finished on 15-Oct-2026. Short-lead mechanical materials show 8,272 earned man-hours against a budget of 8,236.

Open issues and risks

Drawn from the open activities in the P6 update. The weekly report's own issue log is in the workbook, which has no text version.

ISSUE	AREA	DETAIL
Road works on the critical path	Site infrastructure	782 of 1,136 man-hours earned (68.8%). Curb stones, interlock tiles and road signs are in progress at 0%. Geotextile, gravel bedding, traffic lines and wheel bumpers have not started. All have zero float.
Fences and gates behind plan	Site infrastructure	912 of 1,360 man-hours earned (67.1%) against 90.0% planned. Base plates, steel members, steel fence and gates have not started, with 0.8 to 1.8 days of float.
External electrical works	Site infrastructure	88.7% against 100% planned. Earthing (20%) and street-lighting feeder pillars and kWh meters (0%) are in progress, with 2.8 days of float.
Architectural finishing	Blocks A to E	Steel railings, furniture and identification signs remain in every block, with 2.8 to 9.8 days of float.
Close-out and handover	Project close-out	As-built drawings, warranties, training and manuals are due between 19 and 27 Oct with 3.8 days of float. Snag rectification, initial handover and the handover letter (31-Oct-2026 to 02-Nov-2026) have zero float.

Data notes

- The weekly report workbook (No. 41, dated 19-Oct-2026) has no text version in MD Files. Its figures for the S-curve, manpower, cost and invoicing, and health, safety and quality could not be used, so those sections are left out. Contractor, consultant and project manager are not named in any text file. Only its photos were used.
- This report uses only the latest upload (W4), so no previous-week figures are available: progress this week and the this-week column show "–".
- Physical progress comes from the P6 labour units in the P6 update report: 116,740 budgeted, 112,642 planned and 113,420 earned man-hours.
- The file names use project code HAL1-05-009, while the P6 update file is coded HAL1-05-10.
- The P6 update file gives a planned start of 14-Mar-2023, while the project started on 04-Dec-2025. Its start and finish dates for completed activities are later than their actual dates (for example, project start 29-Dec-2025 against 04-Dec-2025 actual).
- Procurement earned and planned man-hours (27,496) exceed its budget (27,460), because the short-lead mechanical purchase orders show 2,480 earned against 2,444 budgeted.
- The "Completion of Engineering and Materials" milestone is still open in P6, forecast for 19-Oct-2026, although all engineering and procurement activities have actual finishes.
- Asphalt wearing course and tack coat show 100% complete but are still marked in progress, with no actual finish.
- Block B's discipline totals add up to 10,655 earned man-hours, against 10,654 on the block line (rounding).
- Report week: the weekly report states its number as 41. Counting whole weeks from project start (04-Dec-2025) to the data date gives week 45.
- The photos carry a camera date stamp of 18-Oct-2026 and no GPS stamp.

Compiled 28-Oct-2026 from the latest weekly upload (W4): P6 update and P6 reports for weekly report No. 41, data date 19-Oct-2026.
