
Development of Phase One – Part Two – Third Industrial

Activity ID	Activity Name	BL Project Duration	BL Project Start	BL Project Finish	Start	Finish	Budgeted Total Cost	Earned Value Cost	Schedule % Complete	Performance % Complete
Development of Phase One – Part Two – Third Industrial City in Dammam - 01-C		730	19-May-25	18-May-27	19-May-25 A	24-Oct-27	,776,076.78	,730,386.15	88.47%	75.6%
Milestones		730	19-May-25	18-May-27	19-May-25 A	24-Oct-27	$0.00	$0.00	0%	0%
MIL-0001	Site Handover	0	19-May-25		19-May-25 A		$0.00	$0.00	100%	100%
MIL-0002	Site Preparations	0		17-Jun-25		17-Jun-25 A	$0.00	$0.00	100%	100%
MIL-0003	Submission of Report, Work Plan, and Schedule	0		17-Jul-25		03-Oct-26	$0.00	$0.00	100%	0%
MIL-0004	Submission and Approval of Drawings and Specifications	0		16-Jul-25		08-Oct-26*	$0.00	$0.00	100%	0%
MIL-0005	Completion of Water Networks and Tanks	0		18-Jan-26		31-Dec-26*	$0.00	$0.00	100%	0%
MIL-0006	Completion of Rainwater Drainage Works	0		18-Jan-26		31-Dec-26*	$0.00	$0.00	100%	0%
MIL-0007	Completion of All Project Services	0		18-May-27		19-Oct-27*	$0.00	$0.00	0%	0%
MIL-0008	Final Handover	0		18-May-27		24-Oct-27	$0.00	$0.00	0%	0%
Mobilization		87	19-May-25	13-Aug-25	19-May-25 A	22-Dec-26	$0.00	$0.00	0%	0%
Mobilization		30	19-May-25	17-Jun-25	19-May-25 A	25-Jun-25 A	$0.00	$0.00	0%	0%
A1070	Mobilization of Manpower	30	19-May-25	17-Jun-25	19-May-25 A	25-Jun-25 A	$0.00	$0.00	100%	100%
A1080	Mobilization of Equipment	30	19-May-25	17-Jun-25	19-May-25 A	25-Jun-25 A	$0.00	$0.00	100%	100%
Deliverables		70	19-May-25	13-Aug-25	19-May-25 A	22-Dec-26	$0.00	$0.00	0%	0%
Submittals		60	19-May-25	02-Aug-25	19-May-25 A	10-Dec-26	$0.00	$0.00	0%	0%
S10001	Prepare & Submit Organization Chart	15	19-May-25	04-Jun-25	29-May-25 A	29-May-25 A	$0.00	$0.00	100%	100%
S100010	Prepare & Submit Mobilization plan	10	19-May-25	29-May-25	19-May-25 A	16-Jul-25 A	$0.00	$0.00	100%	100%
S100011	Prepare & Submit Interface management plan	30	19-May-25	28-Jun-25	16-Jan-26 A	18-Jan-26 A	$0.00	$0.00	100%	100%
S100012	Prepare & Submit Document Control Plan	15	19-May-25	04-Jun-25	23-Aug-25 A	24-Aug-25 A	$0.00	$0.00	100%	100%
S100013	Prepare & Submit Site Security Management Plan	20	19-May-25	16-Jun-25	19-May-25 A	15-Jul-25 A	$0.00	$0.00	100%	100%
S100014	Prepare & Submit Emergency Response Plan	20	19-May-25	16-Jun-25	19-May-25 A	14-Jul-25 A	$0.00	$0.00	100%	100%
S100015	Prepare & Submit Pre-commissioning/ Commissioning Plan/ Startup/ Testing / Handover	60	19-May-25	02-Aug-25	03-Oct-26	10-Dec-26	$0.00	$0.00	100%	0%
S100016	Prepare & Submit Operability and Maintainability Plan	20	19-May-25	16-Jun-25	23-Aug-25 A	24-Aug-25 A	$0.00	$0.00	100%	100%
S10002	Prepare & Submit Method of Statement	20	19-May-25	16-Jun-25	19-May-25 A	06-Oct-26	$0.00	$0.00	100%	80%
S10003	Prepare & Submit Quality plan	20	19-May-25	16-Jun-25	19-May-25 A	24-Jun-25 A	$0.00	$0.00	100%	100%
S10004	Prepare & Submit Construction Environmental Management Plan (CEMP)	25	19-May-25	22-Jun-25	19-May-25 A	03-Sep-25 A	$0.00	$0.00	100%	100%
S10005	Prepare & Submit Safety plan	20	19-May-25	16-Jun-25	19-May-25 A	19-Jun-25 A	$0.00	$0.00	100%	100%
S10006	Prepare & Submit Contractual Project Time Schedule	37	19-May-25	06-Jul-25	19-May-25 A	05-Aug-25 A	$0.00	$0.00	100%	100%
S10007	Prepare & Submit Performance Bond	14	19-May-25	03-Jun-25	19-May-25 A	19-May-25 A	$0.00	$0.00	100%	100%
S10008	Prepare & Submit Insurance	14	19-May-25	03-Jun-25	19-May-25 A	17-Jul-25 A	$0.00	$0.00	100%	100%
S10009	Prepare & Submit Procurement Plan	30	19-May-25	28-Jun-25	01-Oct-25 A	01-Oct-25 A	$0.00	$0.00	100%	100%
Approvals		60	31-May-25	13-Aug-25	19-May-25 A	22-Dec-26	$0.00	$0.00	0%	0%
S100026	Approval of Organization Chart	10	11-Jun-25	22-Jun-25	18-Oct-25 A	19-Oct-25 A	$0.00	$0.00	100%	100%
S100036	Approval of Mobilization plan	10	31-May-25	16-Jun-25	31-May-25 A	21-Jul-25 A	$0.00	$0.00	100%	100%
S100046	Approval of Interface management plan	10	29-Jun-25	09-Jul-25	17-Jan-26 A	23-Jan-26 A	$0.00	$0.00	100%	100%
S100056	Approval of Document Control Plan	10	11-Jun-25	22-Jun-25	23-Aug-25 A	24-Aug-25 A	$0.00	$0.00	100%	100%
S100066	Approval of Site Security Management Plan	10	17-Jun-25	28-Jun-25	17-Jun-25 A	29-Jul-25 A	$0.00	$0.00	100%	100%
S100076	Approval of Emergency Response Plan	10	17-Jun-25	28-Jun-25	18-Oct-25 A	20-Oct-25 A	$0.00	$0.00	100%	100%
S100086	Approval of Pre-commissioning/ Commissioning Plan/ Startup/ Testing / Handover Plan	10	03-Aug-25	13-Aug-25	12-Dec-26	22-Dec-26	$0.00	$0.00	100%	0%
S100096	Approval of Operability and Maintainability Plan	10	17-Jun-25	28-Jun-25	23-Aug-25 A	24-Aug-25 A	$0.00	$0.00	100%	100%
S100106	Approval of Method of Statement	10	17-Jun-25	28-Jun-25	17-Jul-25 A	12-Oct-26	$0.00	$0.00	100%	50%
S100116	Approval of Quality plan	10	17-Jun-25	28-Jun-25	17-Jun-25 A	21-Jul-25 A	$0.00	$0.00	100%	100%
S100126	Approval of Construction Environmental Management Plan (CEMP)	10	23-Jun-25	03-Jul-25	03-Sep-25 A	10-Sep-25 A	$0.00	$0.00	100%	100%
S100136	Approval of Safety plan	10	17-Jun-25	28-Jun-25	02-Oct-25 A	02-Oct-25 A	$0.00	$0.00	100%	100%
S100146	Approval of Contractual Project Time Schedule	10	07-Jul-25	17-Jul-25	31-Jul-25 A	12-Aug-25 A	$0.00	$0.00	100%	100%
S100156	Approval of Performance Bond	10	04-Jun-25	21-Jun-25	19-May-25 A	19-May-25 A	$0.00	$0.00	100%	100%
S100166	Approval of Insurance	10	04-Jun-25	21-Jun-25	04-Jun-25 A	17-Jul-25 A	$0.00	$0.00	100%	100%

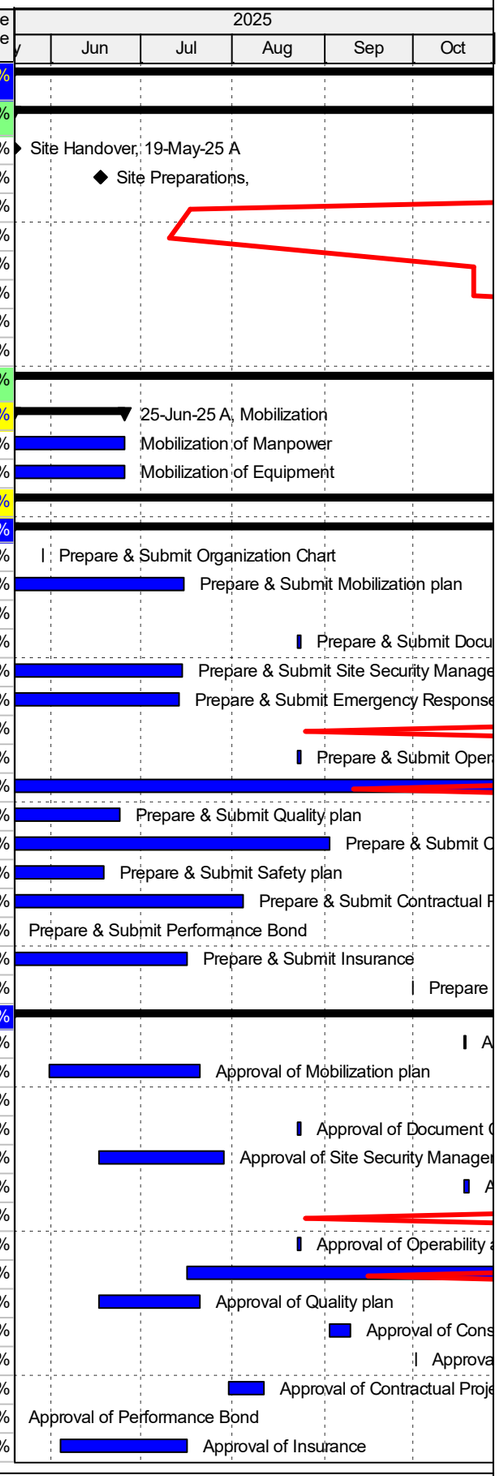

Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary

TASK filter: All Activities

© Oracle Corporation

Development of Phase One – Part Two – Third Industrial

2026 | 2027 | 2028

Nov | Dec | Jan | Feb | Mar | Apr | May | Jun | Jul | Aug | Sep | Oct | Nov | Dec | Jan | Feb | Mar | Apr | May | Jun | Jul | Aug | Sep | Oct | Nov | Dec | Jan

24-Oct-27, Development of Phas

24-Oct-27, Milestones

Submission of Report, Work Plan, and Schedule,

Submission and Approval of Drawings and Specifications,

Completion of Water Networks and Tanks,

Completion of Rainwater Drainage Works,

Completion of All Project Services,

Final Handover,

22-Dec-26, Mobilization

22-Dec-26, Deliverables

10-Dec-26, Submittals

Prepare & Submit Interface management plan

ment Control Plan

ment Plan

e Plan

Prepare & Submit Pre-commissioning/ Commissioning Plan/ Startup/ Testing / Handover Plan

ability and Maintainability Plan

Prepare & Submit Method of Statement

onstruction Environmental Management Plan (CEMP)

Project Time Schedule

& Submit Procurement Plan

22-Dec-26, Approvals

pproval of Organization Chart

Approval of Interface management plan

Control Plan

ment Plan

pproval of Emergency Response Plan

Approval of Pre-commissioning/ Commissioning Plan/ Startup/ Testing / Handover Plan

and Maintainability Plan

Approval of Method of Statement

truction Environmental Management Plan (CEMP)

l of Safety plan

ct Time Schedule


Actual Level of Effort | Actual Work | Remaining Work | Critical Remaining Work | Milestone | summary

TASK filter: All Activities

© Oracle Corporation

Development of Phase One – Part Two – Third Industrial

Activity ID	Activity Name	BL Project Duration	BL Project Start	BL Project Finish	Start	Finish	Budgeted Total Cost	Earned Value Cost	Schedule % Complete	Performance % Complete
S100176	Approval of Procurement Plan	10	29-Jun-25	09-Jul-25	02-Oct-25 A	02-Oct-25 A	$0.00	$0.00	100%	100%
Engineering		374	19-May-25	08-Nov-26	20-May-25 A	14-Oct-26	7,013,282.3	6,869,101.7	98.52%	97.94%
Shop Drawing		43	19-May-25	16-Jul-25	20-May-25 A	08-Oct-26	$0.00	$0.00	0%	0%
Submittals		33	19-May-25	02-Jul-25	20-May-25 A	01-Apr-26 A	$0.00	$0.00	0%	0%
A1550	Earthworks details submittal	33	19-May-25	02-Jul-25	20-May-25 A	21-Jul-25 A	$0.00	$0.00	100%	100%
A1560	Roadworks details submittal	33	19-May-25	02-Jul-25	20-May-25 A	21-Jul-25 A	$0.00	$0.00	100%	100%
A1580	Landscape details submittal	33	19-May-25	02-Jul-25	01-Jan-26 A	01-Apr-26 A	$0.00	$0.00	100%	100%
A1590	Electrical details submittal	33	19-May-25	02-Jul-25	20-May-25 A	21-Jul-25 A	$0.00	$0.00	100%	100%
A1620	Mechanical details submittal	33	19-May-25	02-Jul-25	20-May-25 A	01-Sep-25 A	$0.00	$0.00	100%	100%
Approvals		10	03-Jul-25	16-Jul-25	06-Jul-25 A	08-Oct-26	$0.00	$0.00	0%	0%
A1600	Earthworks details approval	10	03-Jul-25	16-Jul-25	06-Jul-25 A	28-Aug-25 A	$0.00	$0.00	100%	100%
A1610	Roadworks details approval	10	03-Jul-25	16-Jul-25	06-Jul-25 A	28-Aug-25 A	$0.00	$0.00	100%	100%
A1630	Landscape details approval	10	03-Jul-25	16-Jul-25	01-Mar-26 A	08-Oct-26	$0.00	$0.00	100%	50%
A1640	Electrical details approval	10	03-Jul-25	16-Jul-25	06-Jul-25 A	28-Aug-25 A	$0.00	$0.00	100%	100%
A1650	Mechanical details approval	10	03-Jul-25	16-Jul-25	06-Jul-25 A	01-Sep-25 A	$0.00	$0.00	100%	100%
Material Submittal & Approval		350	22-Jun-25	08-Nov-26	26-May-25 A	14-Oct-26	7,013,282.3	6,869,101.7	98.52%	97.94%
Long Lead Items		174	22-Jun-25	19-Feb-26	18-Jun-25 A	07-Oct-26	2,869,511.8	2,807,204.8	100%	97.83%
Pipes (DI / GRP) - For potable, irrigation, sewer, storm		18	03-Jul-25	28-Jul-25	18-Jun-25 A	22-Jul-25 A	$179,398.95	$179,398.95	100%	100%
Drainage Channel Covers (GRP / DI) - For storm and wastewater		24	03-Jul-25	05-Aug-25	18-Jun-25 A	24-Jul-25 A	1,308,857.0	1,308,857.0	100%	100%
Manholes (Precast / Cast in situ) - All networks		20	03-Jul-25	30-Jul-25	20-Jul-25 A	29-Jul-25 A	$356,500.61	$356,500.61	100%	100%
Control & Instrumentation Devices - Flow meters, pressure sensors		20	03-Jul-25	30-Jul-25	20-Jul-25 A	02-Sep-25 A	$46,453.40	$46,453.40	100%	100%
Pumps (Sewage, Irrigation, Booster) - Especially for pumping stations		20	22-Jun-25	17-Jul-25	12-Aug-25 A	16-Oct-25 A	$525,232.91	$525,232.91	100%	100%
Lighting Poles & Fixtures - External works, Roads, PS		20	03-Jul-25	30-Jul-25	03-Jul-25 A	07-Aug-25 A	$90,001.15	$90,001.15	100%	100%
Generators & Fuel Tanks - PS & Control Bldg backup power		20	03-Jul-25	30-Jul-25	20-Jul-25 A	07-Oct-26	$311,534.63	$249,227.70	100%	80%
Cable Trays / Electrical Panels (MCC) - PS and Control Buildings		20	22-Jan-26	19-Feb-26	20-Jul-25 A	24-Aug-25 A	$11,656.73	$11,656.73	100%	100%
Odor Control Units - Sewer PS-specific		20	16-Nov-25	11-Dec-25	22-Jul-25 A	13-Aug-25 A	$39,876.38	$39,876.38	100%	100%
Short Lead Items		341	03-Jul-25	08-Nov-26	26-May-25 A	14-Oct-26	4,143,770.5	4,061,896.8	97.5%	98.02%
Asphalt		20	11-Oct-26	08-Nov-26	05-Aug-25 A	21-Sep-25 A	$103,594.66	$103,594.66	0%	100%
Pipes (HDPE / uPVC) - For potable, irrigation, sewer, storm		20	03-Jul-25	30-Jul-25	26-May-25 A	24-Jun-25 A	1,496,527.7	1,496,527.7	100%	100%
Valves (Gate, Air, NRV, Flow Control) - All water & drainage systems		20	03-Jul-25	30-Jul-25	03-Jul-25 A	02-May-26 A	$123,222.89	$123,222.89	100%	100%
Chambers (Valve / Flowmeter / Washout) - Sewer, Potable, Irrigation		20	03-Jul-25	30-Jul-25	15-Jul-25 A	05-Aug-25 A	$284,016.32	$284,016.32	100%	100%
Communication Ducts & Manholes - Telecom systems		20	03-Jun-26	01-Jul-26	16-Jul-25 A	03-Aug-25 A	$64,045.09	$64,045.09	100%	100%
Air Vents / Washout Assemblies - Water networks		31	03-Jul-25	14-Aug-25	17-Jul-25 A	02-Oct-25 A	$36,002.07	$36,002.07	100%	100%
Warning Tapes, Marker Posts - All underground works		20	03-Jul-25	30-Jul-25	01-Sep-25 A	01-Sep-25 A	$0.00	$0.00	0%	0%
Concrete (for culverts, pads, plinths) - Structural support works		31	03-Jul-25	14-Aug-25	27-Jul-25 A	07-Aug-25 A	1,207,542.1	1,207,542.1	100%	100%
Steel (Rebar, Gratings, Ladders, Covers) - Structural & drainage items		20	03-Jul-25	30-Jul-25	05-Jul-25 A	16-Jul-25 A	$524,731.72	$524,731.72	100%	100%
Interlock Tiles / Curbstone - Roads, Sidewalks, Landscape		20	01-Feb-26	03-Mar-26	01-Feb-26 A	13-Oct-26	$40,886.85	$32,709.48	100%	80%
Landscaping Materials (Soil, Plants) - Final works, softscape		20	01-Feb-26	03-Mar-26	13-Aug-25 A	14-Oct-26	$263,201.00	$189,504.72	100%	72%
Procurement		502	19-May-25	25-Jan-27	19-May-25 A	01-Feb-27	13,038,834.7	11,076,553.6	96.09%	95.44%
Prequalification		411	19-May-25	11-Oct-26	19-May-25 A	07-Oct-26	$0.00	$0.00	0%	0%
Long Lead Items		207	19-May-25	21-Jan-26	19-May-25 A	26-Dec-25 A	$0.00	$0.00	0%	0%
Pipes (DI / GRP) - For potable, irrigation, sewer, storm		34	19-May-25	02-Jul-25	19-May-25 A	24-Jun-25 A	$0.00	$0.00	0%	0%
Drainage Channel Covers (GRP / DI) - For storm and wastewater		34	19-May-25	02-Jul-25	19-May-25 A	24-Jun-25 A	$0.00	$0.00	0%	0%
Manholes (Precast / Cast in situ) - All networks		34	19-May-25	02-Jul-25	19-May-25 A	30-Jul-25 A	$0.00	$0.00	0%	0%
Control & Instrumentation Devices - Flow meters, pressure sensors		34	19-May-25	02-Jul-25	19-May-25 A	30-Jul-25 A	$0.00	$0.00	0%	0%
Pumps (Sewage, Irrigation, Booster) - Especially for pumping stations		34	19-May-25	02-Jul-25	18-Oct-25 A	19-Oct-25 A	$0.00	$0.00	0%	0%
Lighting Poles & Fixtures - External works, Roads, PS		34	19-May-25	02-Jul-25	19-May-25 A	02-Aug-25 A	$0.00	$0.00	0%	0%
Generators & Fuel Tanks - PS & Control Bldg backup power		34	19-May-25	02-Jul-25	19-May-25 A	02-Aug-25 A	$0.00	$0.00	0%	0%
Cable Trays / Electrical Panels (MCC) - PS and Control Buildings		34	14-Dec-25	21-Jan-26	26-Sep-25 A	26-Dec-25 A	$0.00	$0.00	0%	0%
Odor Control Units - Sewer PS-specific		31	09-Oct-25	13-Nov-25	05-Aug-25 A	09-Sep-25 A	$0.00	$0.00	0%	0%
Short Lead Items		411	19-May-25	11-Oct-26	19-May-25 A	07-Oct-26	$0.00	$0.00	0%	0%
Asphalt		34	31-Aug-26	11-Oct-26	17-Jul-25 A	09-Sep-25 A	$0.00	$0.00	0%	0%

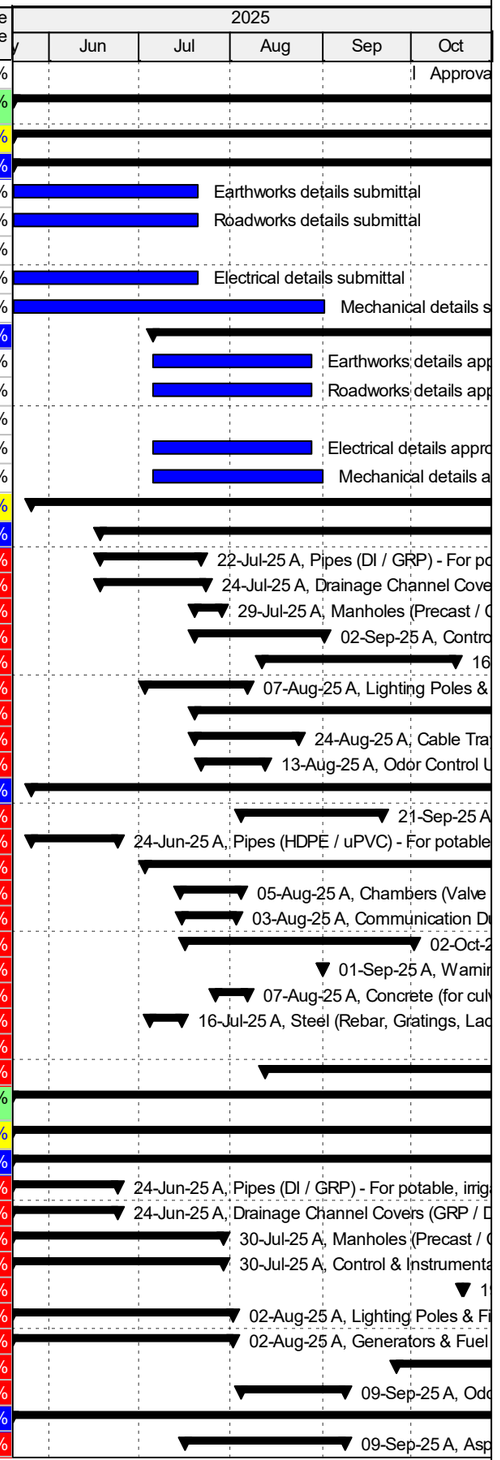

© Oracle Corporation

Development of Phase One – Part Two – Third Industrial

2026 | 2027 | 2028

Nov | Dec | Jan | Feb | Mar | Apr | May | Jun | Jul | Aug | Sep | Oct | Nov | Dec | Jan | Feb | Mar | Apr | May | Jun | Jul | Aug | Sep | Oct | Nov | Dec | Jan

of Procurement Plan
14-Oct-26, Engineering
08-Oct-26, Shop Drawing
01-Apr-26 A, Submittals
Landscape details submittal
ubmittal
08-Oct-26, Approvals
roval
roval
Landscape details approval
val
pproval
14-Oct-26, Material Submittal & Approval
07-Oct-26, Long Lead Items
table, irrigation, sewer, storm
rs (GRP / DI) - For storm and wastewater
ast in situ) - All networks
& Instrumentation Devices - Flow meters, pressure sensors
Oct-25 A, Pumps (Sewage, Irrigation, Booster) - Especially for pumping stations
Fixtures - External works, Roads, PS
07-Oct-26, Generators & Fuel Tanks - PS & Control Bldg backup power
s / Electrical Panels (MCC) - PS and Control Buildings
nits - Sewer PS-specific
14-Oct-26, Short Lead Items
Asphalt
irrigation, sewer, storm
02-May-26 A, Valves (Gate, Air, NRV, Flow Control) - All water & drainage systems
Flowmeter / Washout) - Sewer, Potable, Irrigation
cts & Manholes - Telecom systems
5 A, Air Vents / Washout Assemblies - Water networks
g Tapes, Marker Posts - All underground works
erts, pads, plinths) - Structural support works
ders, Covers) - Structural & drainage items
13-Oct-26, Interlock Tiles / Curbstone - Roads, Sidewalks, Landscape
14-Oct-26, Landscaping Materials (Soil, Plants) - Final works, softscape
01-Feb-27, Procurement
07-Oct-26, Prequalification
26-Dec-25 A, Long Lead Items
ation, sewer, storm
l) - For storm and wastewater
Cast in situ) - All networks
tion Devices - Flow meters, pressure sensors
9-Oct-25 A, Pumps (Sewage, Irrigation, Booster) - Especially for pumping stations
ktures - External works, Roads, PS
Tanks - PS & Control Bldg backup power
26-Dec-25 A, Cable Trays / Electrical Panels (MCC) - PS and Control Buildings
r Control Units - Sewer PS-specific
07-Oct-26, Short Lead Items
halt


Actual Level of Effort | Remaining Work | Milestone
Actual Work | Critical Remaining Work | summary

TASK filter: All Activities

© Oracle Corporation

Development of Phase One – Part Two – Third Industrial

Activity ID	Activity Name	BL Project Duration	BL Project Start	BL Project Finish	Start	Finish	Budgeted Total Cost	Earned Value Cost	Schedule % Complete	Performance % Complete
	Pipes (HDPE / uPVC) - For potable, irrigation, sewer, storm	34	19-May-25	02-Jul-25	19-May-25 A	24-Jun-25 A	$0.00	$0.00	0%	0%
	Valves (Gate, Air, NRV, Flow Control) - All water & drainage systems	34	19-May-25	02-Jul-25	19-May-25 A	03-Aug-25 A	$0.00	$0.00	0%	0%
	Chambers (Valve / Flowmeter / Washout) - Sewer, Potable, Irrigation	34	19-May-25	02-Jul-25	19-May-25 A	03-Aug-25 A	$0.00	$0.00	0%	0%
	Communication Ducts & Manholes - Telecom systems	34	20-Apr-26	03-Jun-26	02-Aug-25 A	03-Aug-25 A	$0.00	$0.00	0%	0%
	Air Vents / Washout Assemblies - Water networks	34	19-May-25	02-Jul-25	19-May-25 A	03-Aug-25 A	$0.00	$0.00	0%	0%
	Warning Tapes, Marker Posts - All underground works	34	19-May-25	02-Jul-25	18-Jul-25 A	25-Sep-25 A	$0.00	$0.00	0%	0%
	Concrete (for culverts, pads, plinths) - Structural support works	34	19-May-25	02-Jul-25	19-May-25 A	24-Jun-25 A	$0.00	$0.00	0%	0%
	Steel (Rebar, Gratings, Ladders, Covers) - Structural & drainage items	34	19-May-25	02-Jul-25	19-May-25 A	14-Jul-25 A	$0.00	$0.00	0%	0%
	Interlock Tiles / Curbstone - Roads, Sidewalks, Landscape	34	22-Dec-25	29-Jan-26	21-Feb-26 A	07-Oct-26	$0.00	$0.00	0%	0%
	Landscaping Materials (Soil, Plants) - Final works, softscape	34	22-Dec-25	29-Jan-26	13-Aug-25 A	07-Oct-26	$0.00	$0.00	0%	0%
	Long Lead Items	387	19-Jul-25	07-Nov-26	02-Aug-25 A	30-Nov-26	17,609,507.(	17,271,293.9	99.99%	98.08%
	Pipes (DI / GRP) - For potable, irrigation, sewer, storm	99	29-Jul-25	22-Nov-25	02-Aug-25 A	06-Jan-26 A	1,100,928.4	1,100,928.4	100%	100%
A102480	Issue PO for Pipes (DI / GRP) - For potable, irrigation, sewer, storm	4	29-Jul-25	02-Aug-25	02-Aug-25 A	05-Aug-25 A	$0.00	$0.00	100%	100%
A102490	Manufacturing for Pipes (DI / GRP) - For potable, irrigation, sewer, storm	30	03-Aug-25	06-Sep-25	06-Aug-25 A	05-Jan-26 A	$0.00	$0.00	100%	100%
A102500	Delivery for Pipes (DI / GRP) - For potable, irrigation, sewer, storm	30	13-Sep-25	18-Oct-25	20-Sep-25 A	05-Jan-26 A	1,100,928.4	1,100,928.4	100%	100%
A102550	Custom Clearance for Pipes (DI / GRP) - For potable, irrigation, sewer, storm	5	07-Sep-25	11-Sep-25	17-Sep-25 A	06-Jan-26 A	$0.00	$0.00	100%	100%
A102560	Staging Time for Pipes (DI / GRP) - For potable, irrigation, sewer, storm	30	19-Oct-25	22-Nov-25	20-Sep-25 A	05-Jan-26 A	$0.00	$0.00	100%	100%
	Drainage Channel Covers (GRP / DI) - For storm and wastewater	129	06-Aug-25	04-Jan-26	05-Nov-25 A	04-Oct-26	8,032,142.3	7,951,820.9	100%	99%
A102570	Custom Clearance for Drainage Channel Covers (GRP / DI) - For storm and wastewater	10	21-Oct-25	01-Nov-25	17-Nov-25 A	03-Oct-26	$0.00	$0.00	100%	99%
A102580	Staging Time for Drainage Channel Covers (GRP / DI) - For storm and wastewater	30	01-Dec-25	04-Jan-26	01-Jan-26 A	04-Oct-26	$0.00	$0.00	100%	99%
A1220	Issue PO for Drainage Channel Covers (GRP / DI) - For storm and wastewater	4	06-Aug-25	10-Aug-25	05-Nov-25 A	06-Dec-25 A	$0.00	$0.00	100%	100%
A1230	Manufacturing for Drainage Channel Covers (GRP / DI) - For storm and wastewater	60	11-Aug-25	20-Oct-25	19-Nov-25 A	03-Oct-26	$0.00	$0.00	100%	99%
A1240	Delivery for Drainage Channel Covers (GRP / DI) - For storm and wastewater	25	02-Nov-25	30-Nov-25	23-Nov-25 A	03-Oct-26	8,032,142.3	7,951,820.9	100%	99%
	Manholes (Precast / Cast in situ) - All networks	119	31-Jul-25	17-Dec-25	16-Sep-25 A	21-May-26 A	2,187,758.8	2,187,758.8	100%	100%
A102590	Custom Clearance for Manholes (Precast / Cast in situ) - All networks	10	28-Sep-25	08-Oct-25	20-Sep-25 A	04-May-26 A	$0.00	$0.00	100%	100%
A102600	Staging Time for Manholes (Precast / Cast in situ) - All networks	30	13-Nov-25	17-Dec-25	11-Nov-25 A	21-May-26 A	$0.00	$0.00	100%	100%
A1460	Issue PO for Manholes (Precast / Cast in situ) - All networks	4	31-Jul-25	04-Aug-25	16-Sep-25 A	16-Sep-25 A	$0.00	$0.00	100%	100%
A1470	Manufacturing for Manholes (Precast / Cast in situ) - All networks	45	05-Aug-25	27-Sep-25	16-Sep-25 A	01-May-26 A	$0.00	$0.00	100%	100%
A1480	Delivery for Manholes (Precast / Cast in situ) - All networks	30	09-Oct-25	12-Nov-25	21-Sep-25 A	16-May-26 A	2,187,758.8	2,187,758.8	100%	100%
	Control & Instrumentation Devices - Flow meters, pressure sensors	119	31-Jul-25	17-Dec-25	24-Aug-25 A	29-Oct-26	$285,073.41	$270,819.74	100%	95%
A102610	Custom Clearance for Control & Instrumentation Devices - Flow meters, pressure sensor	5	28-Sep-25	02-Oct-25	26-Nov-25 A	04-Oct-26	$0.00	$0.00	100%	96%
A102620	Staging Time for Control & Instrumentation Devices - Flow meters, pressure sensors	30	13-Nov-25	17-Dec-25	16-Apr-26 A	29-Oct-26	$0.00	$0.00	100%	35%
A1520	Issue PO for Control & Instrumentation Devices - Flow meters, pressure sensors	4	31-Jul-25	04-Aug-25	24-Aug-25 A	24-Aug-25 A	$0.00	$0.00	100%	100%
A1530	Manufacturing for Control & Instrumentation Devices - Flow meters, pressure sensors	45	05-Aug-25	27-Sep-25	24-Aug-25 A	04-Oct-26	$0.00	$0.00	100%	96%
A1570	Delivery for Control & Instrumentation Devices - Flow meters, pressure sensors	35	04-Oct-25	12-Nov-25	13-Apr-26 A	06-Oct-26	$285,073.41	$270,819.74	100%	95%
	Pumps (Sewage, Irrigation, Booster) - Especially for pumping stations	129	19-Jul-25	16-Dec-25	16-Oct-25 A	07-Oct-26	3,223,228.6	3,094,299.5	100%	96%
A102140	Issue PO for Pumps (Sewage, Irrigation, Booster) - Especially for pumping stations	4	19-Jul-25	22-Jul-25	16-Oct-25 A	16-Oct-25 A	$0.00	$0.00	100%	100%
A102150	Manufacturing for Pumps (Sewage, Irrigation, Booster) - Especially for pumping stations	45	23-Jul-25	13-Sep-25	16-Oct-25 A	03-Oct-26	$0.00	$0.00	100%	98%
A102170	Delivery for Pumps (Sewage, Irrigation, Booster) - Especially for pumping stations	45	20-Sep-25	11-Nov-25	05-Nov-25 A	05-Oct-26	3,223,228.6	3,094,299.5	100%	96%
A102630	Custom Clearance for Pumps (Sewage, Irrigation, Booster) - Especially for pumping stati	5	14-Sep-25	18-Sep-25	28-Nov-25 A	04-Oct-26	$0.00	$0.00	100%	96%
A102640	Staging Time for Pumps (Sewage, Irrigation, Booster) - Especially for pumping stations	30	12-Nov-25	16-Dec-25	20-Jan-26 A	07-Oct-26	$0.00	$0.00	100%	96%
	Lighting Poles & Fixtures - External works, Roads, PS	124	31-Jul-25	23-Dec-25	10-Oct-25 A	12-Jan-26 A	$552,315.51	$552,315.51	100%	100%
A102650	Custom Clearance for Lighting Poles & Fixtures - External works, Roads, PS	5	15-Oct-25	20-Oct-25	27-Nov-25 A	14-Dec-25 A	$0.00	$0.00	100%	100%
A102660	Staging Time for Lighting Poles & Fixtures - External works, Roads, PS	30	19-Nov-25	23-Dec-25	02-Dec-25 A	12-Jan-26 A	$0.00	$0.00	100%	100%
A1400	Issue PO for Lighting Poles & Fixtures - External works, Roads, PS	4	31-Jul-25	04-Aug-25	10-Oct-25 A	11-Oct-25 A	$0.00	$0.00	100%	100%
A1410	Manufacturing for Lighting Poles & Fixtures - External works, Roads, PS	60	05-Aug-25	14-Oct-25	29-Nov-25 A	03-Dec-25 A	$0.00	$0.00	100%	100%
A1420	Delivery for Lighting Poles & Fixtures - External works, Roads, PS	25	21-Oct-25	18-Nov-25	30-Nov-25 A	09-Dec-25 A	$552,315.51	$552,315.51	100%	100%
	Generators & Fuel Tanks - PS & Control Bldg backup power	115	31-Jul-25	13-Dec-25	05-Dec-25 A	26-Oct-26	1,911,813.4	1,797,104.6	100%	94%
A102220	Issue PO for Generators & Fuel Tanks - PS & Control Bldg backup power	4	31-Jul-25	04-Aug-25	05-Dec-25 A	10-Dec-25 A	$0.00	$0.00	100%	100%
A102230	Manufacturing for Generators & Fuel Tanks - PS & Control Bldg backup power	55	05-Aug-25	08-Oct-25	08-Dec-25 A	11-Oct-26	$0.00	$0.00	100%	96%

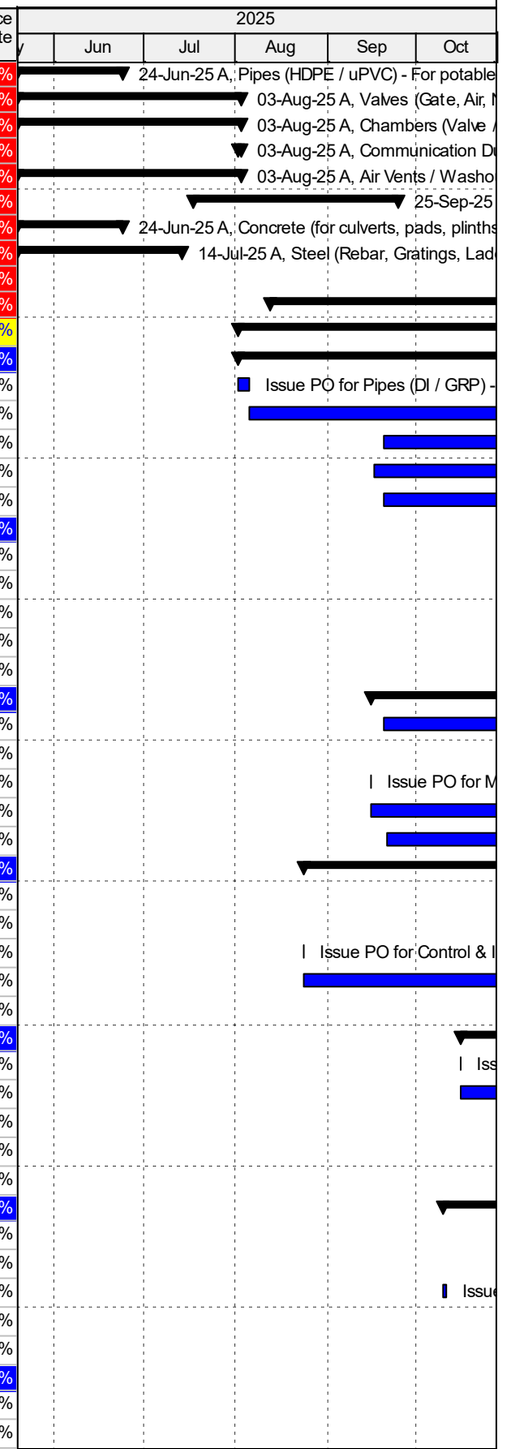

© Oracle Corporation

Development of Phase One – Part Two – Third Industrial

2026 | 2027 | 2028

Nov | Dec | Jan | Feb | Mar | Apr | May | Jun | Jul | Aug | Sep | Oct | Nov | Dec | Jan | Feb | Mar | Apr | May | Jun | Jul | Aug | Sep | Oct | Nov | Dec | Jan

irrigation, sewer, storm
NRV, Flow Control) - All water & drainage systems
Flowmeter / Washout) - Sewer, Potable, Irrigation
ucts & Manholes - Telecom systems
ut Assemblies - Water networks
A, Warning Tapes, Marker Posts - All underground works
) - Structural support works
ders, Covers) - Structural & drainage items

07-Oct-26, Interlock Tiles / Curbstone - Roads, Sidewalks, Landscape
07-Oct-26, Landscaping Materials (Soil, Plants) - Final works, softscape
30-Nov-26, Long Lead Items
06-Jan-26 A, Pipes (DI / GRP) - For potable, irrigation, sewer, storm
For potable, irrigation, sewer, storm
Manufacturing for Pipes (DI / GRP) - For potable, irrigation, sewer, storm
Delivery for Pipes (DI / GRP) - For potable, irrigation, sewer, storm
Custom Clearance for Pipes (DI / GRP) - For potable, irrigation, sewer, storm
Staging Time for Pipes (DI / GRP) - For potable, irrigation, sewer, storm
04-Oct-26, Drainage Channel Covers (GRP / DI) - For storm and wastewater
Custom Clearance for Drainage Channel Covers (GRP / DI) - For storm and wastewater
Staging Time for Drainage Channel Covers (GRP / DI) - For storm and wastewater
Issue PO for Drainage Channel Covers (GRP / DI) - For storm and wastewater
Manufacturing for Drainage Channel Covers (GRP / DI) - For storm and wastewater
Delivery for Drainage Channel Covers (GRP / DI) - For storm and wastewater
21-May-26 A, Manholes (Precast / Cast in situ) - All networks
Custom Clearance for Manholes (Precast / Cast in situ) - All networks
Staging Time for Manholes (Precast / Cast in situ) - All networks
anholes (Precast / Cast in situ) - All networks
Manufacturing for Manholes (Precast / Cast in situ) - All networks
Delivery for Manholes (Precast / Cast in situ) - All networks
29-Oct-26, Control & Instrumentation Devices - Flow meters, pressure sensors
Custom Clearance for Control & Instrumentation Devices - Flow meters, pressure sensors
Staging Time for Control & Instrumentation Devices - Flow meters, pressure sensors
nstrumentation Devices - Flow meters, pressure sensors
Manufacturing for Control & Instrumentation Devices - Flow meters, pressure sensors
Delivery for Control & Instrumentation Devices - Flow meters, pressure sensors
07-Oct-26, Pumps (Sewage, Irrigation, Booster) - Especially for pumping stations
ue PO for Pumps (Sewage, Irrigation, Booster) - Especially for pumping stations
Manufacturing for Pumps (Sewage, Irrigation, Booster) - Especially for pumping stations
Delivery for Pumps (Sewage, Irrigation, Booster) - Especially for pumping stations
Custom Clearance for Pumps (Sewage, Irrigation, Booster) - Especially for pumping stations
Staging Time for Pumps (Sewage, Irrigation, Booster) - Especially for pumping stations
12-Jan-26 A, Lighting Poles & Fixtures - External works, Roads, PS
Custom Clearance for Lighting Poles & Fixtures - External works, Roads, PS
Staging Time for Lighting Poles & Fixtures - External works, Roads, PS
e PO for Lighting Poles & Fixtures - External works, Roads, PS
Manufacturing for Lighting Poles & Fixtures - External works, Roads, PS
Delivery for Lighting Poles & Fixtures - External works, Roads, PS
26-Oct-26, Generators & Fuel Tanks - PS & Control Bldg backup power
Issue PO for Generators & Fuel Tanks - PS & Control Bldg backup power
Manufacturing for Generators & Fuel Tanks - PS & Control Bldg backup power


Actual Level of Effort | Actual Work | Remaining Work | Critical Remaining Work | Milestone | summary

TASK filter: All Activities

© Oracle Corporation

Development of Phase One – Part Two – Third Industrial

Activity ID	Activity Name	BL Project Duration	BL Project Start	BL Project Finish	Start	Finish	Budgeted Total Cost	Earned Value Cost	Schedule % Complete	Performance % Complete
A102250	Delivery for Generators & Fuel Tanks - PS & Control Bldg backup power	21	15-Oct-25	08-Nov-25	10-Dec-25 A	12-Oct-26	1,911,813.4	1,797,104.6	100%	94%
A102670	Custom Clearance for Generators & Fuel Tanks - PS & Control Bldg backup power	5	09-Oct-25	14-Oct-25	01-Jan-26 A	11-Oct-26	$0.00	$0.00	100%	93%
A102680	Staging Time for Generators & Fuel Tanks - PS & Control Bldg backup power	30	09-Nov-25	13-Dec-25	04-Jul-26 A	26-Oct-26	$0.00	$0.00	100%	60%
Cable Trays / Electrical Panels (MCC) - PS and Control Buildings		204	19-Feb-26	07-Nov-26	24-Aug-25 A	23-Oct-25 A	$71,534.55	$71,534.55	98.33%	100%
A102200	Issue PO for Cable Trays / Electrical Panels (MCC) - PS and Control Buildings	4	19-Feb-26	01-Mar-26	24-Aug-25 A	24-Aug-25 A	$0.00	$0.00	100%	100%
A102210	Manufacturing for Cable Trays / Electrical Panels (MCC) - PS and Control Buildings	90	01-Mar-26	30-Jun-26	24-Aug-25 A	24-Aug-25 A	$0.00	$0.00	100%	100%
A102240	Delivery for Cable Trays / Electrical Panels (MCC) - PS and Control Buildings	60	25-Jul-26	03-Oct-26	10-Oct-25 A	11-Oct-25 A	$71,534.55	$71,534.55	98.33%	100%
A102690	Custom Clearance for Cable Trays / Electrical Panels (MCC) - PS and Control Buildings	20	01-Jul-26	23-Jul-26	24-Aug-25 A	24-Aug-25 A	$0.00	$0.00	100%	100%
A102700	Staging Time for Cable Trays / Electrical Panels (MCC) - PS and Control Buildings	30	04-Oct-26	07-Nov-26	10-Oct-25 A	23-Oct-25 A	$0.00	$0.00	0%	100%
Odor Control Units - Sewer PS-specific		204	14-Dec-25	31-Aug-26	09-Nov-25 A	30-Nov-26	$244,711.80	$244,711.80	100%	100%
A102120	Issue PO for Odor Control Units - Sewer PS-specific	4	14-Dec-25	17-Dec-25	09-Nov-25 A	30-Nov-25 A	$0.00	$0.00	100%	100%
A102130	Manufacturing for Odor Control Units - Sewer PS-specific	90	18-Dec-25	20-Apr-26	01-Jan-26 A	04-May-26 A	$0.00	$0.00	100%	100%
A102180	Delivery for Odor Control Units - Sewer PS-specific	60	13-May-26	27-Jul-26	01-Apr-26 A	21-May-26 A	$244,711.80	$244,711.80	100%	100%
A102710	Custom Clearance for Odor Control Units - Sewer PS-specific	20	20-Apr-26	13-May-26	01-Apr-26 A	13-Apr-26 A	$0.00	$0.00	100%	100%
A102720	Staging Time for Odor Control Units - Sewer PS-specific	30	27-Jul-26	31-Aug-26	26-Oct-26	30-Nov-26	$0.00	$0.00	100%	0%
Short Lead Items		444	31-Jul-25	25-Jan-27	25-Jul-25 A	01-Feb-27	25,429,327.6	23,805,259.6	93.38%	93.61%
Asphalt		67	08-Nov-26	25-Jan-27	19-Nov-25 A	01-Dec-26	$635,735.66	$629,378.30	0%	99%
A102730	Delivery for Asphalt Phase 1	21	12-Nov-26	07-Dec-26	01-Dec-25 A	01-Dec-26	$211,911.89	$209,792.77	0%	99%
A103740	Delivery for Asphalt Phase 2	21	07-Dec-26	31-Dec-26	08-Dec-25 A	01-Dec-26	$211,911.89	$209,792.77	0%	99%
A103750	Delivery for Asphalt Phase 3	21	31-Dec-26	25-Jan-27	14-Dec-25 A	01-Dec-26	$211,911.89	$209,792.77	0%	99%
A1160	Issue PO for Asphalt	4	08-Nov-26	12-Nov-26	19-Nov-25 A	30-Nov-25 A	$0.00	$0.00	0%	100%
Pipes (HDPE / uPVC) - For potable, irrigation, sewer, storm		84	31-Jul-25	06-Nov-25	01-Aug-25 A	14-Jan-26 A	9,183,832.7	9,183,832.7	100%	100%
A102100	Issue PO for Pipes (HDPE / uPVC) - For potable, irrigation, sewer, storm	4	31-Jul-25	04-Aug-25	01-Aug-25 A	06-Aug-25 A	$0.00	$0.00	100%	100%
A102110	Manufacturing for Pipes (HDPE / uPVC) - For potable, irrigation, sewer, storm	30	05-Aug-25	08-Sep-25	06-Aug-25 A	14-Dec-25 A	$0.00	$0.00	100%	100%
A102190	Delivery for Pipes (HDPE / uPVC) - For potable, irrigation, sewer, storm	20	09-Sep-25	02-Oct-25	10-Aug-25 A	08-Dec-25 A	9,183,832.7	9,183,832.7	100%	100%
A102740	Staging Time for Pipes (HDPE / uPVC) - For potable, irrigation, sewer, storm	30	04-Oct-25	06-Nov-25	01-Jan-26 A	14-Jan-26 A	$0.00	$0.00	100%	100%
Valves (Gate, Air, NRV, Flow Control) - All water & drainage systems		109	31-Jul-25	06-Dec-25	25-Nov-25 A	13-Apr-26 A	$756,189.36	$756,189.36	100%	100%
A102080	Issue PO for Valves (Gate, Air, NRV, Flow Control) - All water & drainage systems	4	31-Jul-25	04-Aug-25	25-Nov-25 A	01-Dec-25 A	$0.00	$0.00	100%	100%
A102090	Manufacturing for Valves (Gate, Air, NRV, Flow Control) - All water & drainage systems	60	05-Aug-25	14-Oct-25	26-Nov-25 A	01-Mar-26 A	$0.00	$0.00	100%	100%
A102160	Delivery for Valves (Gate, Air, NRV, Flow Control) - All water & drainage systems	15	15-Oct-25	01-Nov-25	01-Dec-25 A	30-Mar-26 A	$756,189.36	$756,189.36	100%	100%
A102750	Staging Time for Valves (Gate, Air, NRV, Flow Control) - All water & drainage systems	30	02-Nov-25	06-Dec-25	01-Feb-26 A	13-Apr-26 A	$0.00	$0.00	100%	100%
Chambers (Valve / Flowmeter / Washout) - Sewer, Potable, Irrigation		94	31-Jul-25	18-Nov-25	10-Nov-25 A	31-Mar-26 A	1,742,940.1	1,742,940.1	100%	100%
A101970	Issue PO for Chambers (Valve / Flowmeter / Washout) - Sewer, Potable, Irrigation	4	31-Jul-25	04-Aug-25	10-Nov-25 A	14-Nov-25 A	$0.00	$0.00	100%	100%
A101980	Manufacturing for Chambers (Valve / Flowmeter / Washout) - Sewer, Potable, Irrigation	30	05-Aug-25	08-Sep-25	17-Nov-25 A	01-Feb-26 A	$0.00	$0.00	100%	100%
A102030	Delivery for Chambers (Valve / Flowmeter / Washout) - Sewer, Potable, Irrigation	30	09-Sep-25	14-Oct-25	24-Nov-25 A	02-Mar-26 A	1,742,940.1	1,742,940.1	100%	100%
A102760	Staging Time for Chambers (Valve / Flowmeter / Washout) - Sewer, Potable, Irrigation	30	15-Oct-25	18-Nov-25	01-Jan-26 A	31-Mar-26 A	$0.00	$0.00	100%	100%
Communication Ducts & Manholes - Telecom systems		109	31-Aug-26	06-Jan-27	24-Aug-25 A	16-Jan-27 A	$393,029.41	$393,029.41	0%	100%
A101990	Issue PO for Communication Ducts & Manholes - Telecom systems	4	31-Aug-26	05-Sep-26	24-Aug-25 A	31-Aug-25 A	$0.00	$0.00	100%	100%
A102000	Manufacturing for Communication Ducts & Manholes - Telecom systems	45	05-Sep-26	28-Oct-26	24-Aug-25 A	10-Jan-26 A	$0.00	$0.00	49.33%	100%
A102050	Delivery for Communication Ducts & Manholes - Telecom systems	30	28-Oct-26	02-Dec-26	24-Nov-25 A	16-Jan-27 A	$393,029.41	$393,029.41	0%	100%
A102770	Staging Time for Communication Ducts & Manholes - Telecom systems	30	02-Dec-26	06-Jan-27	01-Dec-26 A	22-Dec-26 A	$0.00	$0.00	0%	100%
Air Vents / Washout Assemblies - Water networks		109	16-Aug-25	21-Dec-25	13-Dec-25 A	12-May-26 A	$220,936.06	$220,936.06	100%	100%
A102410	Issue PO for Air Vents / Washout Assemblies - Water networks	4	16-Aug-25	19-Aug-25	13-Dec-25 A	14-Dec-25 A	$0.00	$0.00	100%	100%
A102420	Manufacturing for Air Vents / Washout Assemblies - Water networks	45	20-Aug-25	12-Oct-25	15-Dec-25 A	01-Apr-26 A	$0.00	$0.00	100%	100%
A102460	Delivery for Air Vents / Washout Assemblies - Water networks	30	13-Oct-25	16-Nov-25	01-Jan-26 A	02-May-26 A	$220,936.06	$220,936.06	100%	100%
A102780	Staging Time for Air Vents / Washout Assemblies - Water networks	30	17-Nov-25	21-Dec-25	01-Feb-26 A	12-May-26 A	$0.00	$0.00	100%	100%
Warning Tapes, Marker Posts - All underground works		74	31-Jul-25	26-Oct-25	30-Sep-25 A	15-Dec-25 A	$0.00	$0.00	0%	0%
A102260	Issue PO for Warning Tapes, Marker Posts - All underground works	4	31-Jul-25	04-Aug-25	30-Sep-25 A	30-Sep-25 A	$0.00	$0.00	100%	100%
A102270	Manufacturing for Warning Tapes, Marker Posts - All underground works	19	05-Aug-25	26-Aug-25	30-Sep-25 A	30-Sep-25 A	$0.00	$0.00	100%	100%

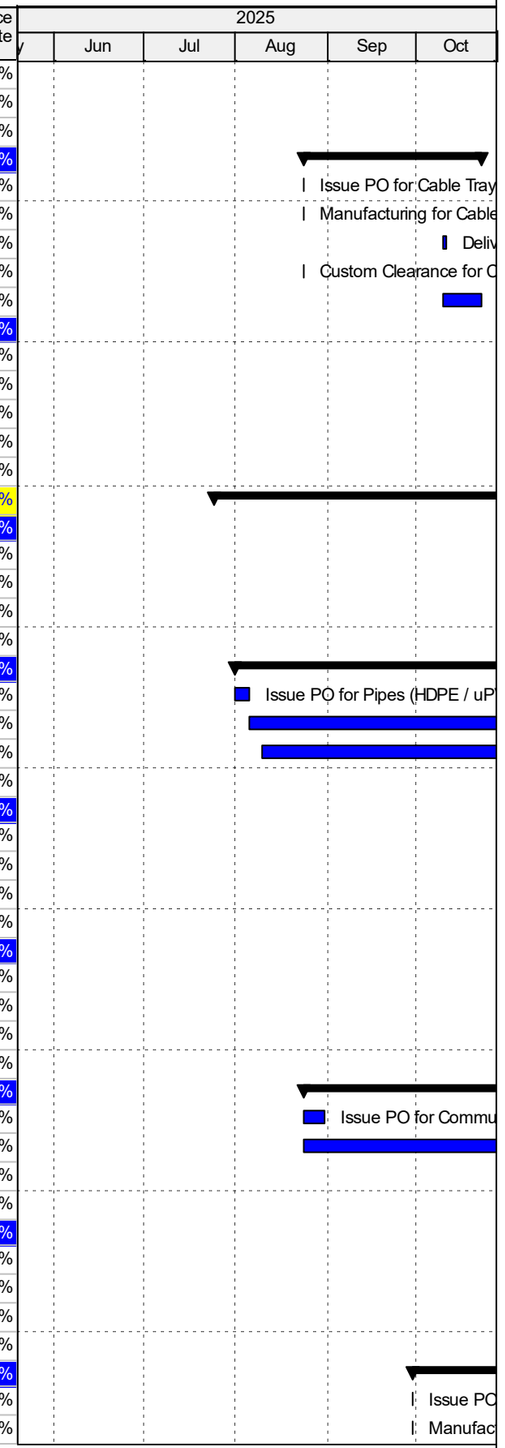

© Oracle Corporation

Development of Phase One – Part Two – Third Industrial

2026 | 2027 | 2028

Nov | Dec | Jan | Feb | Mar | Apr | May | Jun | Jul | Aug | Sep | Oct | Nov | Dec | Jan | Feb | Mar | Apr | May | Jun | Jul | Aug | Sep | Oct | Nov | Dec | Jan

Delivery for Generators & Fuel Tanks - PS & Control Bldg backup power
Custom Clearance for Generators & Fuel Tanks - PS & Control Bldg backup power
Staging Time for Generators & Fuel Tanks - PS & Control Bldg backup power
23-Oct-25 A, Cable Trays / Electrical Panels (MCC) - PS and Control Buildings
s / Electrical Panels (MCC) - PS and Control Buildings
Trays / Electrical Panels (MCC) - PS and Control Buildings
ery for Cable Trays / Electrical Panels (MCC) - PS and Control Buildings
able Trays / Electrical Panels (MCC) - PS and Control Buildings
Staging Time for Cable Trays / Electrical Panels (MCC) - PS and Control Buildings
30-Nov-26, Odor Control Units - Sewer PS-specific
Issue PO for Odor Control Units - Sewer PS-specific
Manufacturing for Odor Control Units - Sewer PS-specific
Delivery for Odor Control Units - Sewer PS-specific
Custom Clearance for Odor Control Units - Sewer PS-specific
Staging Time for Odor Control Units - Sewer PS-specific
01-Feb-27, Short Lead Items
01-Dec-26, Asphalt
Delivery for Asphalt Phase 1
Delivery for Asphalt Phase 2
Delivery for Asphalt Phase 3
Issue PO for Asphalt
14-Jan-26 A, Pipes (HDPE / uPVC) - For potable, irrigation, sewer, storm
VC) - For potable, irrigation, sewer, storm
Manufacturing for Pipes (HDPE / uPVC) - For potable, irrigation, sewer, storm
Delivery for Pipes (HDPE / uPVC) - For potable, irrigation, sewer, storm
Staging Time for Pipes (HDPE / uPVC) - For potable, irrigation, sewer, storm
13-Apr-26 A, Valves (Gate, Air, NRV, Flow Control) - All water & drainage systems
Issue PO for Valves (Gate, Air, NRV, Flow Control) - All water & drainage systems
Manufacturing for Valves (Gate, Air, NRV, Flow Control) - All water & drainage systems
Delivery for Valves (Gate, Air, NRV, Flow Control) - All water & drainage systems
Staging Time for Valves (Gate, Air, NRV, Flow Control) - All water & drainage systems
31-Mar-26 A, Chambers (Valve / Flowmeter / Washout) - Sewer, Potable, Irrigation
Issue PO for Chambers (Valve / Flowmeter / Washout) - Sewer, Potable, Irrigation
Manufacturing for Chambers (Valve / Flowmeter / Washout) - Sewer, Potable, Irrigation
Delivery for Chambers (Valve / Flowmeter / Washout) - Sewer, Potable, Irrigation
Staging Time for Chambers (Valve / Flowmeter / Washout) - Sewer, Potable, Irrigation
16-Jan-27 A, Communication Ducts & Manholes - Telecom systems
nication Ducts & Manholes - Telecom systems
Manufacturing for Communication Ducts & Manholes - Telecom systems
Delivery for Communication Ducts & Manholes - Telecom systems
Staging Time for Communication Ducts & Manholes - Telecom systems
12-May-26 A, Air Vents / Washout Assemblies - Water networks
Issue PO for Air Vents / Washout Assemblies - Water networks
Manufacturing for Air Vents / Washout Assemblies - Water networks
Delivery for Air Vents / Washout Assemblies - Water networks
Staging Time for Air Vents / Washout Assemblies - Water networks
15-Dec-25 A, Warning Tapes, Marker Posts - All underground works
for Warning Tapes, Marker Posts - All underground works
uring for Warning Tapes, Marker Posts - All underground works


Actual Level of Effort | Actual Work | Remaining Work | Critical Remaining Work | Milestone | summary

TASK filter: All Activities

© Oracle Corporation

Development of Phase One – Part Two – Third Industrial

Activity ID	Activity Name	BL Project Duration	BL Project Start	BL Project Finish	Start	Finish	Budgeted Total Cost	Earned Value Cost	Schedule % Complete	Performance % Complete
A102320	Delivery for Warning Tapes, Marker Posts - All underground works	21	27-Aug-25	20-Sep-25	30-Sep-25 A	04-Oct-25 A	$0.00	$0.00	100%	100%
A102790	Staging Time for Warning Tapes, Marker Posts - All underground works	30	21-Sep-25	26-Oct-25	13-Dec-25 A	15-Dec-25 A	$0.00	$0.00	100%	100%
Concrete (for culverts, pads, plinths) - Structural support works		364	16-Aug-25	08-Nov-26	30-Jul-25 A	15-Jun-26 A	7,410,396.9	7,410,396.9	91.17%	100%
A102280	Issue PO for Concrete (for culverts, pads, plinths) - Structural support works	4	16-Aug-25	19-Aug-25	30-Jul-25 A	30-Jul-25 A	$0.00	$0.00	100%	100%
A102340	Delivery for Concrete (for culverts, pads, plinths) - Structural support works P1	30	20-Aug-25	24-Sep-25	25-Nov-25 A	06-Dec-25 A	$617,533.08	$617,533.08	100%	100%
A103760	Delivery for Concrete (for culverts, pads, plinths) - Structural support works P2	30	25-Sep-25	29-Oct-25	03-Dec-25 A	11-Dec-25 A	$617,533.08	$617,533.08	100%	100%
A103770	Delivery for Concrete (for culverts, pads, plinths) - Structural support works P3	30	30-Oct-25	03-Dec-25	09-Dec-25 A	10-Dec-25 A	$617,533.08	$617,533.08	100%	100%
A103780	Delivery for Concrete (for culverts, pads, plinths) - Structural support works P4	30	04-Dec-25	07-Jan-26	15-Dec-25 A	01-Jan-26 A	$617,533.08	$617,533.08	100%	100%
A103790	Delivery for Concrete (for culverts, pads, plinths) - Structural support works P5	30	08-Jan-26	11-Feb-26	01-Jan-26 A	08-Jan-26 A	$617,533.08	$617,533.08	100%	100%
A103800	Delivery for Concrete (for culverts, pads, plinths) - Structural support works P6	30	12-Feb-26	06-Apr-26	17-Jan-26 A	22-Jan-26 A	$617,533.08	$617,533.08	100%	100%
A103810	Delivery for Concrete (for culverts, pads, plinths) - Structural support works P7	30	06-Apr-26	11-May-26	17-Jan-26 A	29-Jan-26 A	$617,533.08	$617,533.08	100%	100%
A103820	Delivery for Concrete (for culverts, pads, plinths) - Structural support works P8	30	11-May-26	20-Jun-26	01-Feb-26 A	12-Feb-26 A	$617,533.08	$617,533.08	100%	100%
A103830	Delivery for Concrete (for culverts, pads, plinths) - Structural support works P9	30	20-Jun-26	25-Jul-26	01-Mar-26 A	31-Mar-26 A	$617,533.08	$617,533.08	100%	100%
A103840	Delivery for Concrete (for culverts, pads, plinths) - Structural support works P10	30	25-Jul-26	29-Aug-26	31-Mar-26 A	21-Apr-26 A	$617,533.08	$617,533.08	100%	100%
A103850	Delivery for Concrete (for culverts, pads, plinths) - Structural support works P11	30	29-Aug-26	04-Oct-26	01-Apr-26 A	14-Apr-26 A	$617,533.08	$617,533.08	94%	100%
A103860	Delivery for Concrete (for culverts, pads, plinths) - Structural support works P12	30	04-Oct-26	08-Nov-26	01-May-26 A	15-Jun-26 A	$617,533.08	$617,533.08	0%	100%
Steel (Rebar, Gratings, Ladders, Covers) - Structural & drainage items		62	31-Jul-25	12-Oct-25	25-Jul-25 A	17-Jun-26 A	3,220,152.9	3,220,152.9	100%	100%
A102300	Issue PO for Steel (Rebar, Gratings, Ladders, Covers) - Structural & drainage items	4	31-Jul-25	04-Aug-25	25-Jul-25 A	25-Jul-25 A	$0.00	$0.00	100%	100%
A102310	Manufacturing for Steel (Rebar, Gratings, Ladders, Covers) - Structural & drainage items	21	05-Aug-25	28-Aug-25	25-Jul-25 A	20-May-26 A	$0.00	$0.00	100%	100%
A102330	Delivery for Steel (Rebar, Gratings, Ladders, Covers) - Structural & drainage items	7	30-Aug-25	06-Sep-25	10-Aug-25 A	13-Jun-26 A	3,220,152.9	3,220,152.9	100%	100%
A102810	Staging Time for Steel (Rebar, Gratings, Ladders, Covers) - Structural & drainage items	30	07-Sep-25	12-Oct-25	12-Nov-25 A	17-Jun-26 A	$0.00	$0.00	100%	100%
Interlock Tiles / Curbstone - Roads, Sidewalks, Landscape		94	03-Mar-26	07-Jul-26	03-Nov-25 A	02-Nov-26	$250,912.80	$248,403.67	100%	99%
A102370	Issue PO for Interlock Tiles / Curbstone - Roads, Sidewalks, Landscape	4	03-Mar-26	10-Mar-26	03-Nov-25 A	14-Nov-25 A	$0.00	$0.00	100%	100%
A102380	Manufacturing for Interlock Tiles / Curbstone - Roads, Sidewalks, Landscape	30	11-Mar-26	23-Apr-26	01-Jan-26 A	13-Oct-26	$0.00	$0.00	100%	99%
A102400	Delivery for Interlock Tiles / Curbstone - Roads, Sidewalks, Landscape	30	23-Apr-26	02-Jun-26	01-Apr-26 A	14-Oct-26	$250,912.80	$248,403.67	100%	99%
A102820	Staging Time for Interlock Tiles / Curbstone - Roads, Sidewalks, Landscape	30	02-Jun-26	07-Jul-26	04-Jul-26 A	02-Nov-26	$0.00	$0.00	100%	45%
Landscaping Materials (Soil, Plants) - Final works, softscape		94	03-Mar-26	07-Jul-26	14-Oct-26	01-Feb-27	1,615,201.5	$0.00	100%	0%
A102350	Issue PO for Landscaping Materials (Soil, Plants) - Final works, softscape	4	03-Mar-26	10-Mar-26	14-Oct-26	19-Oct-26	$0.00	$0.00	100%	0%
A102360	Manufacturing for Landscaping Materials (Soil, Plants) - Final works, softscape	60	11-Mar-26	02-Jun-26	19-Oct-26	28-Dec-26	$0.00	$0.00	100%	0%
A102390	Delivery for Landscaping Materials (Soil, Plants) - Final works, softscape	30	02-Jun-26	07-Jul-26	28-Dec-26	01-Feb-27	1,615,201.5	$0.00	100%	0%
Construction		729	19-May-25	18-May-27	19-May-25 A	19-Oct-27	60,346,352.	16,355,189.	89.87%	72.56%
Zone 3		440	13-Oct-25	26-Dec-26	15-Sep-25 A	30-Jun-27	30,801,187.7	12,697,137.4	97.32%	64.36%
Sewerage Network Zone 3		440	13-Oct-25	26-Dec-26	01-Jan-26 A	17-Apr-27	6,994,093.4	2,013,913.9	84.12%	28.79%
Pipework: Supply, Installation, and Testing		101	19-Oct-25	27-Jan-26	01-Jan-26 A	26-Oct-26	$369,724.94	$353,055.57	100%	95.49%
Fittings and Valves		27	14-Dec-25	13-Jan-26	03-Oct-26	02-Nov-26	$30,711.20	$0.00	100%	0%
Valve & Flow Meter Chambers		115	19-Oct-25	10-Feb-26	08-Jun-26 A	14-Dec-26	$49,924.39	$17,953.74	100%	35.96%
Manholes		137	19-Oct-25	04-Mar-26	01-Jan-26 A	03-Dec-26	$849,279.83	$642,540.77	100%	75.66%
Pumping Stations		356	13-Oct-25	26-Dec-26	13-Jan-26 A	17-Apr-27	5,694,453.0	1,000,363.8	80.5%	17.57%
Rainwater Drainage Network Zone 3		92	19-Oct-25	18-Jan-26	05-Jan-26 A	26-Nov-26	10,744,160.0	7,503,593.8	100%	69.84%
Pipe Laying Works		92	19-Oct-25	18-Jan-26	05-Jan-26 A	01-Nov-26	$591,302.61	$503,268.09	100%	85.11%
Precast Concrete Box Culverts		78	19-Oct-25	18-Jan-26	01-Mar-26 A	26-Nov-26	1,156,736.8	$441,213.10	100%	38.14%
Manholes		36	07-Dec-25	18-Jan-26	15-Oct-26	26-Nov-26	$780,038.12	$0.00	100%	0%
Chambers and Catch Basins		35	07-Dec-25	17-Jan-26	18-Jan-26 A	21-Oct-26	$607,967.93	$580,102.66	100%	95.42%
Gully Outfalls to Swales		18	28-Dec-25	18-Jan-26	01-Feb-26 A	05-Nov-26	$176,898.27	$107,554.15	100%	60.8%
Backfilling & Bedding		66	02-Nov-25	18-Jan-26	17-Mar-26 A	26-Oct-26	2,298,195.3	2,028,106.3	100%	88.25%
Deep Basin for Groundwater Collection (2.5–3.0m)		59	10-Nov-25	18-Jan-26	02-Feb-26 A	26-Oct-26	5,133,020.9	3,843,349.4	100%	74.88%
Potable Water Network Zone 3		92	19-Oct-25	18-Jan-26	13-Oct-25 A	22-Dec-26	12,325,662.8	5,698,715.0	100%	46.23%
Pipe Installation Works		57	19-Oct-25	14-Dec-25	01-Jan-26 A	13-Oct-26	1,002,366.1	$671,585.31	100%	67%
Valve Installation & Chambers		61	09-Nov-25	18-Jan-26	02-Jun-26 A	27-Oct-26	$316,303.42	$245,261.67	100%	77.54%
Flow Meter Installation		45	20-Nov-25	11-Jan-26	12-Aug-26 A	23-Nov-26	$61,536.16	$19,383.89	100%	31.5%
Washout & Air Valve Chambers		48	09-Nov-25	03-Jan-26	01-Aug-26 A	12-Oct-26	$304,525.24	$238,753.17	100%	78.4%

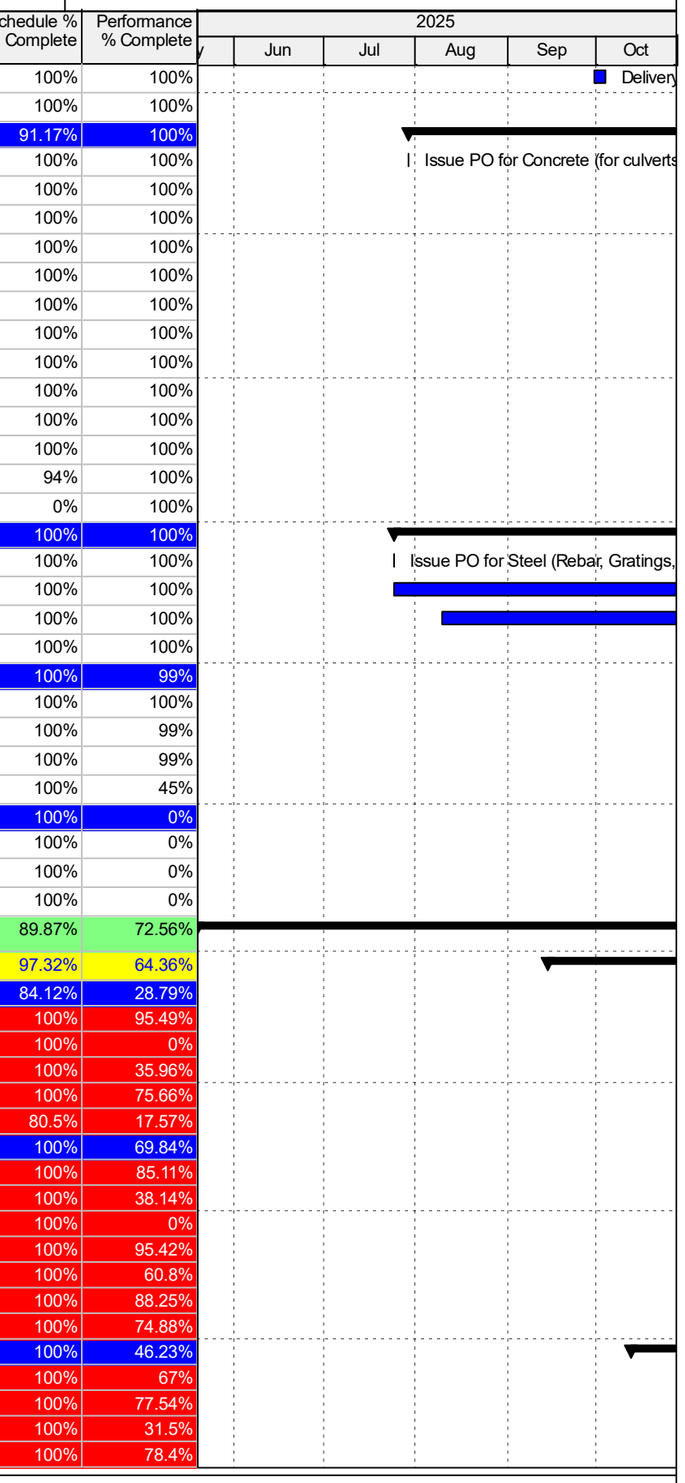

© Oracle Corporation

Development of Phase One – Part Two – Third Industrial

2026 | 2027 | 2028

Nov | Dec | Jan | Feb | Mar | Apr | May | Jun | Jul | Aug | Sep | Oct | Nov | Dec | Jan | Feb | Mar | Apr | May | Jun | Jul | Aug | Sep | Oct | Nov | Dec | Jan

for Warning Tapes, Marker Posts - All underground works
Staging Time for Warning Tapes, Marker Posts - All underground works
15-Jun-26 A, Concrete (for culverts, pads, plinths) - Structural support works
, pads, plinths) - Structural support works
Delivery for Concrete (for culverts, pads, plinths) - Structural support works P1
Delivery for Concrete (for culverts, pads, plinths) - Structural support works P2
Delivery for Concrete (for culverts, pads, plinths) - Structural support works P3
Delivery for Concrete (for culverts, pads, plinths) - Structural support works P4
Delivery for Concrete (for culverts, pads, plinths) - Structural support works P5
Delivery for Concrete (for culverts, pads, plinths) - Structural support works P6
Delivery for Concrete (for culverts, pads, plinths) - Structural support works P7
Delivery for Concrete (for culverts, pads, plinths) - Structural support works P8
Delivery for Concrete (for culverts, pads, plinths) - Structural support works P9
Delivery for Concrete (for culverts, pads, plinths) - Structural support works P10
Delivery for Concrete (for culverts, pads, plinths) - Structural support works P11
Delivery for Concrete (for culverts, pads, plinths) - Structural support works P12
17-Jun-26 A, Steel (Rebar, Gratings, Ladders, Covers) - Structural & drainage items
Ladders, Covers) - Structural & drainage items
Manufacturing for Steel (Rebar, Gratings, Ladders, Covers) - Structural & drainage items
Delivery for Steel (Rebar, Gratings, Ladders, Covers) - Structural & drainage items
Staging Time for Steel (Rebar, Gratings, Ladders, Covers) - Structural & drainage items
02-Nov-26, Interlock Tiles / Curbstone - Roads, Sidewalks, Landscape
Issue PO for Interlock Tiles / Curbstone - Roads, Sidewalks, Landscape
Manufacturing for Interlock Tiles / Curbstone - Roads, Sidewalks, Landscape
Delivery for Interlock Tiles / Curbstone - Roads, Sidewalks, Landscape
Staging Time for Interlock Tiles / Curbstone - Roads, Sidewalks, Landscape
01-Feb-27, Landscaping Materials (Soil, Plants) - Final works, softscape
Issue PO for Landscaping Materials (Soil, Plants) - Final works, softscape
Manufacturing for Landscaping Materials (Soil, Plants) - Final works, softscape
Delivery for Landscaping Materials (Soil, Plants) - Final works, softscape
19-Oct-27, Construction
30-Jun-27, Zone 3
17-Apr-27, Sewerage Network Zone 3
26-Oct-26, Pipework: Supply, Installation, and Testing
02-Nov-26, Fittings and Valves
14-Dec-26, Valve & Flow Meter Chambers
03-Dec-26, Manholes
17-Apr-27, Pumping Stations
26-Nov-26, Rainwater Drainage Network Zone 3
01-Nov-26, Pipe Laying Works
26-Nov-26, Precast Concrete Box Culverts
26-Nov-26, Manholes
21-Oct-26, Chambers and Catch Basins
05-Nov-26, Gully Outfalls to Swales
26-Oct-26, Backfilling & Bedding
26-Oct-26, Deep Basin for Groundwater Collection (2.5–3.0m)
22-Dec-26, Potable Water Network Zone 3
13-Oct-26, Pipe Installation Works
27-Oct-26, Valve Installation & Chambers
23-Nov-26, Flow Meter Installation
12-Oct-26, Washout & Air Valve Chambers

Actual Level of Effort | Actual Work | Remaining Work | Critical Remaining Work | Milestone | summary

TASK filter: All Activities

© Oracle Corporation

Development of Phase One – Part Two – Third Industrial

Activity ID	Activity Name	BL Project Duration	BL Project Start	BL Project Finish	Start	Finish	Budgeted Total Cost	Earned Value Cost	Schedule % Complete	Performance % Complete
	Pumping Station (Structure & Civil Works)	66	19-Oct-25	04-Jan-26	03-Oct-26	17-Dec-26	$473,145.06	$0.00	100%	0%
	Pump Station Building	31	30-Nov-25	05-Jan-26	14-Nov-26	19-Dec-26	$183,637.93	$0.00	100%	0%
	Pumping Equipment & Fire Systems	28	17-Dec-25	18-Jan-26	14-Nov-26	15-Dec-26	$946,290.12	$0.00	100%	0%
	Surge Protection	5	13-Jan-26	18-Jan-26	10-Dec-26	15-Dec-26	$28,227.66	$0.00	100%	0%
	Power & Generator System	12	03-Jan-26	15-Jan-26	30-Nov-26	13-Dec-26	2,851,518.7	$0.00	100%	0%
	Chlorination System	14	03-Jan-26	18-Jan-26	30-Nov-26	15-Dec-26	$518,457.97	$0.00	100%	0%
	Water Storage System	11	05-Jan-26	18-Jan-26	13-Oct-25 A	22-Dec-26	5,159,570.0	4,127,656.0	100%	80%
	Street Lighting	30	15-Dec-25	18-Jan-26	05-Dec-25 A	07-Dec-26	$480,084.41	$396,074.98	100%	82.5%
	Irrigation Network Zone 3	85	19-Oct-25	11-Jan-26	21-Mar-26 A	15-Nov-26	$832,623.82	$718,393.14	100%	86.28%
	Excavation, Pipe Laying & Backfilling	57	19-Oct-25	14-Dec-25	01-Apr-26 A	09-Oct-26	$546,284.50	$461,064.12	100%	84.4%
	Valves and Appurtenances	19	07-Dec-25	28-Dec-25	14-Jun-26 A	06-Oct-26	$63,598.84	$58,318.24	100%	91.7%
	Valve Rooms	19	11-Dec-25	01-Jan-26	01-May-26 A	03-Oct-26	$60,148.03	$59,696.92	100%	99.25%
	Washout Chambers	29	07-Dec-25	08-Jan-26	13-Apr-26 A	04-Oct-26	$70,306.78	$66,439.91	100%	94.5%
	Air Valve Chambers	27	07-Dec-25	06-Jan-26	21-Mar-26 A	03-Oct-26	$47,448.36	$47,092.49	100%	99.25%
	Flow Meter Chambers	31	07-Dec-25	11-Jan-26	01-Apr-26 A	15-Nov-26	$44,837.31	$25,781.45	100%	57.5%
	Rainwater Collection Ponds Zone 3	236	19-Jan-26	14-Nov-26	15-Sep-25 A	20-Mar-27	19,076,657.7	16,461,810.2	98.76%	86.29%
	Excavation for Rainwater Drainage Pond	37	19-Jan-26	14-Mar-26	01-Oct-25 A	09-Jan-27	$394,641.69	$325,776.71	100%	82.55%
	General Site Preparation	77	22-Jan-26	10-May-26	15-Sep-25 A	05-Jan-27	15,134,572.8	13,717,975.2	100%	90.64%
	Backfilling Works	65	10-May-26	29-Jul-26	18-Nov-25 A	21-Jan-27	$844,533.44	$682,383.02	100%	80.8%
	Geotextile & Bedding	66	01-Jun-26	17-Aug-26	12-Jan-26 A	20-Mar-27	1,432,939.9	$465,705.48	100%	32.5%
	Concrete Structures	45	17-Aug-26	10-Oct-26	07-Apr-26 A	26-Nov-26 A	1,031,983.5	1,031,983.5	97.84%	100%
	Energy Dissipation & Siphon Structures	42	26-Sep-26	14-Nov-26	18-Nov-25 A	01-Dec-26 A	$237,986.24	$237,986.24	9.6%	100%
	Road Crossing Zone 3	206	22-Jan-26	13-Oct-26	01-Apr-26 A	30-Jun-27	$827,989.78	$300,711.19	98.5%	36.32%
	uPVC Road Crossing Pipes	110	22-Jan-26	22-Jun-26	01-Apr-26 A	24-Feb-27	$601,422.38	$300,711.19	100%	50%
	GRP Road Crossing Pipes	96	22-Jun-26	13-Oct-26	24-Feb-27	30-Jun-27	$226,567.41	$0.00	94.5%	0%
Zone 2		416	19-Oct-25	08-Dec-26	15-Oct-25 A	02-Aug-27	31,359,284.0	25,280,286.6	99.09%	80.61%
	Sewerage Network Zone 2	137	19-Oct-25	04-Mar-26	04-Jan-26 A	08-Dec-26	2,599,280.7	1,718,764.2	100%	66.12%
	Pipework: Supply, Installation, and Testing	108	19-Oct-25	03-Feb-26	04-Jan-26 A	25-Nov-26	$739,449.88	$637,141.62	100%	86.16%
	Fittings and Valves	27	21-Dec-25	20-Jan-26	26-Oct-26	26-Nov-26	$61,422.41	$0.00	100%	0%
	Valve & Flow Meter Chambers	115	19-Oct-25	10-Feb-26	01-Jul-26 A	08-Dec-26	$99,848.78	$36,441.43	100%	36.5%
	Manholes	137	19-Oct-25	04-Mar-26	01-Feb-26 A	14-Nov-26	1,698,559.6	1,045,181.1	100%	61.53%
	Rainwater Drainage Network Zone 2	92	19-Oct-25	18-Jan-26	15-Oct-25 A	10-Nov-26	11,222,278.1	8,656,753.3	100%	77.14%
	Pipe Laying Works	92	19-Oct-25	18-Jan-26	26-Nov-25 A	07-Oct-26	1,182,605.2	1,149,278.9	100%	97.18%
	Precast Concrete Box Culverts	79	19-Oct-25	18-Jan-26	01-Apr-26 A	09-Nov-26	2,313,473.6	1,037,200.9	100%	44.83%
	Manholes	32	13-Dec-25	18-Jan-26	01-Jan-26 A	10-Nov-26	1,560,076.2	$695,055.97	100%	44.55%
	Chambers and Catch Basins	32	13-Dec-25	18-Jan-26	15-Oct-25 A	25-Jun-26 A	1,215,935.8	1,215,935.8	100%	100%
	Gully Outfalls to Swales	22	24-Dec-25	18-Jan-26	01-Feb-26 A	25-Oct-26	$353,796.54	$264,993.61	100%	74.9%
	Backfilling & Bedding	55	03-Nov-25	06-Jan-26	01-Dec-25 A	12-Oct-26	4,596,390.6	4,294,288.0	100%	93.43%
	Potable Water Network Zone 2	87	19-Oct-25	13-Jan-26	23-Dec-25 A	25-Nov-26	3,369,461.9	2,947,703.0	100%	87.48%
	Pipe Installation Works	57	19-Oct-25	14-Dec-25	23-Dec-25 A	04-Oct-26	2,004,732.2	1,944,590.2	100%	97%
	Valve Installation & Chambers	46	09-Nov-25	31-Dec-25	01-Apr-26 A	17-Oct-26	$632,606.85	$485,146.19	100%	76.69%
	Flow Meter Installation	45	23-Nov-25	13-Jan-26	30-Aug-26 A	25-Nov-26	$123,072.32	$38,767.78	100%	31.5%
	Washout & Air Valve Chambers	52	09-Nov-25	07-Jan-26	01-May-26 A	12-Oct-26	$609,050.48	$479,198.77	100%	78.68%
	Irrigation Network Zone 2	92	19-Oct-25	18-Jan-26	20-Nov-25 A	08-Nov-26	1,665,247.6	1,525,022.0	100%	91.58%
	Excavation, Pipe Laying & Backfilling	57	19-Oct-25	14-Dec-25	20-Nov-25 A	05-Oct-26	1,092,569.0	1,010,626.3	100%	92.5%
	Valves and Appurtenances	20	07-Dec-25	29-Dec-25	05-Feb-26 A	07-Oct-26	$127,197.68	$104,034.60	100%	81.79%
	Valve Rooms	25	21-Dec-25	18-Jan-26	30-Jan-26 A	04-Oct-26	$120,296.07	$119,093.11	100%	99%
	Washout Chambers	25	21-Dec-25	18-Jan-26	18-Apr-26 A	05-Oct-26	$140,613.57	$134,989.03	100%	96%
	Air Valve Chambers	21	25-Dec-25	18-Jan-26	23-Mar-26 A	28-Jul-26 A	$94,896.71	$94,896.71	100%	100%
	Flow Meter Chambers	25	21-Dec-25	18-Jan-26	01-Apr-26 A	08-Nov-26	$89,674.62	$61,382.28	100%	68.45%
	Rainwater Collection Ponds Zone 2	257	19-Jan-26	08-Dec-26	27-Oct-25 A	01-Apr-27	10,847,036.1	10,432,043.9	97.59%	96.17%
	Excavation for Rainwater Drainage Pond	37	19-Jan-26	14-Mar-26	01-May-26 A	09-Jan-27	$112,754.77	$98,322.16	100%	87.2%
	General Site Preparation	98	22-Jan-26	08-Jun-26	27-Oct-25 A	08-Sep-26 A	9,720,726.1	9,720,726.1	100%	100%
	Backfilling Works	65	08-Jun-26	23-Aug-26	17-Nov-25 A	21-Jan-27	$241,295.27	$184,590.88	100%	76.5%

2025: Jun | Jul | Aug | Sep | Oct

Actual Level of Effort · Actual Work · Remaining Work · Critical Remaining Work · Milestone · summary

TASK filter: All Activities

© Oracle Corporation

Development of Phase One – Part Two – Third Industrial

2026 | 2027 | 2028

Nov | Dec | Jan | Feb | Mar | Apr | May | Jun | Jul | Aug | Sep | Oct | Nov | Dec | Jan | Feb | Mar | Apr | May | Jun | Jul | Aug | Sep | Oct | Nov | Dec | Jan

17-Dec-26, Pumping Station (Structure & Civil Works)
19-Dec-26, Pump Station Building
15-Dec-26, Pumping Equipment & Fire Systems
15-Dec-26, Surge Protection
13-Dec-26, Power & Generator System
15-Dec-26, Chlorination System
22-Dec-26, Water Storage System
07-Dec-26, Street Lighting
15-Nov-26, Irrigation Network Zone 3
09-Oct-26, Excavation, Pipe Laying & Backfilling
06-Oct-26, Valves and Appurtenances
03-Oct-26, Valve Rooms
04-Oct-26, Washout Chambers
03-Oct-26, Air Valve Chambers
15-Nov-26, Flow Meter Chambers
20-Mar-27, Rainwater Collection Ponds Zone 3
09-Jan-27, Excavation for Rainwater Drainage Pond
05-Jan-27, General Site Preparation
21-Jan-27, Backfilling Works
20-Mar-27, Geotextile & Bedding
26-Nov-26 A, Concrete Structures
01-Dec-26 A, Energy Dissipation & Siphon Structures
30-Jun-27, Road Crossing Zone 3
24-Feb-27, uPVC Road Crossing Pipes
30-Jun-27, GRP Road Crossing Pipes
02-Aug-27, Zone 2
08-Dec-26, Sewerage Network Zone 2
25-Nov-26, Pipework: Supply, Installation, and Testing
26-Nov-26, Fittings and Valves
08-Dec-26, Valve & Flow Meter Chambers
14-Nov-26, Manholes
10-Nov-26, Rainwater Drainage Network Zone 2
07-Oct-26, Pipe Laying Works
09-Nov-26, Precast Concrete Box Culverts
10-Nov-26, Manholes
25-Jun-26 A, Chambers and Catch Basins
25-Oct-26, Gully Outfalls to Swales
12-Oct-26, Backfilling & Bedding
25-Nov-26, Potable Water Network Zone 2
04-Oct-26, Pipe Installation Works
17-Oct-26, Valve Installation & Chambers
25-Nov-26, Flow Meter Installation
12-Oct-26, Washout & Air Valve Chambers
08-Nov-26, Irrigation Network Zone 2
05-Oct-26, Excavation, Pipe Laying & Backfilling
07-Oct-26, Valves and Appurtenances
04-Oct-26, Valve Rooms
05-Oct-26, Washout Chambers
28-Jul-26 A, Air Valve Chambers
08-Nov-26, Flow Meter Chambers
01-Apr-27, Rainwater Collection Ponds Zone 2
09-Jan-27, Excavation for Rainwater Drainage Pond
08-Sep-26 A, General Site Preparation
21-Jan-27, Backfilling Works


Actual Level of Effort | Remaining Work | Milestone
Actual Work | Critical Remaining Work | summary

TASK filter: All Activities

© Oracle Corporation

Development of Phase One – Part Two – Third Industrial

Activity ID	Activity Name	BL Project Duration	BL Project Start	BL Project Finish	Start	Finish	Budgeted Total Cost	Earned Value Cost	Schedule % Complete	Performance % Complete
	Geotextile & Bedding	66	25-Jun-26	10-Sep-26	04-Jan-26 A	23-Mar-27	$409,411.41	$98,258.74	100%	24%
	Concrete Structures	45	10-Sep-26	03-Nov-26	02-Mar-26 A	01-Apr-27	$294,852.45	$262,149.99	34.58%	88.91%
	Energy Dissipation & Siphon Structures	42	20-Oct-26	08-Dec-26	09-Dec-25 A	15-Jan-26 A	$67,996.07	$67,996.07	0%	100%
	Road Crossing Zone 2	206	22-Jan-26	13-Oct-26	31-Dec-26	02-Aug-27	1,655,979.5	$0.00	98.5%	0%
	uPVC Road Crossing Pipes	110	22-Jan-26	22-Jun-26	31-Dec-26	07-Apr-27	1,202,844.7	$0.00	100%	0%
	GRP Road Crossing Pipes	96	22-Jun-26	13-Oct-26	08-Apr-27	02-Aug-27	$453,134.81	$0.00	94.5%	0%
	Zone 1	483	13-Oct-25	08-Feb-27	22-Jul-25 A	19-Oct-27	53,088,596.(	18,765,955.7	89.33%	77.3%
	Sewerage Network Zone 1	442	13-Oct-25	28-Dec-26	03-Nov-25 A	08-Mar-27	8,652,451.5	2,582,075.8	49.3%	29.84%
	Pipework: Supply, Installation, and Testing	108	19-Oct-25	03-Feb-26	03-Nov-25 A	10-Oct-26	$739,449.88	$727,989.69	100%	98.45%
	Fittings and Valves	27	21-Dec-25	20-Jan-26	05-Oct-26	05-Nov-26	$61,422.41	$0.00	100%	0%
	Valve & Flow Meter Chambers	115	19-Oct-25	10-Feb-26	01-Jun-26 A	17-Dec-26	$99,848.78	$37,677.75	100%	37.73%
	Manholes	82	19-Oct-25	08-Jan-26	31-Dec-25 A	24-Oct-26	1,698,559.6	1,136,398.7	100%	66.9%
	Pumping Stations	358	13-Oct-25	28-Dec-26	01-Jan-26 A	08-Mar-27	6,053,170.7	$680,009.70	27.53%	11.23%
	Rainwater Drainage Network Zone 1	92	19-Oct-25	18-Jan-26	01-Oct-25 A	02-Nov-26	11,222,278.1	9,286,386.7	100%	82.75%
	Pipe Laying Works	92	19-Oct-25	18-Jan-26	01-Oct-25 A	11-Oct-26	1,182,605.2	1,121,322.9	100%	94.82%
	Precast Concrete Box Culverts	69	19-Oct-25	06-Jan-26	01-Apr-26 A	01-Nov-26	2,313,473.6	1,533,939.8	100%	66.3%
	Manholes	47	25-Nov-25	18-Jan-26	01-Jan-26 A	02-Nov-26	1,560,076.2	1,049,796.6	100%	67.29%
	Chambers and Catch Basins	47	25-Nov-25	18-Jan-26	28-Dec-25 A	10-Oct-26	1,215,935.8	1,213,849.4	100%	99.83%
	Gully Outfalls to Swales	26	20-Dec-25	18-Jan-26	31-Dec-25 A	13-Oct-26	$353,796.54	$314,949.68	100%	89.02%
	Backfilling & Bedding	67	02-Nov-25	18-Jan-26	01-Jan-26 A	19-Oct-26	4,596,390.6	4,052,528.1	100%	88.17%
	Potable Water Network Zone 1	91	19-Oct-25	17-Jan-26	09-Sep-25 A	29-Nov-26	3,369,461.9	2,994,625.6	100%	88.88%
	Pipe Installation Works	57	19-Oct-25	14-Dec-25	09-Sep-25 A	04-Oct-26	2,004,732.2	1,918,528.7	100%	95.7%
	Valve Installation & Chambers	42	09-Nov-25	27-Dec-25	01-Feb-26 A	06-Oct-26	$632,606.85	$543,092.98	100%	85.85%
	Flow Meter Installation	60	09-Nov-25	17-Jan-26	01-May-26 A	29-Nov-26	$123,072.32	$45,044.47	100%	36.6%
	Washout & Air Valve Chambers	51	09-Nov-25	06-Jan-26	01-May-26 A	13-Oct-26	$609,050.48	$487,959.41	100%	80.12%
	Irrigation Network Zone 1	92	19-Oct-25	18-Jan-26	04-Nov-25 A	09-Nov-26	1,665,247.6	1,566,078.6	100%	94.04%
	Excavation, Pipe Laying & Backfilling	57	19-Oct-25	14-Dec-25	04-Nov-25 A	03-Oct-26	1,092,569.0	1,079,458.1	100%	98.8%
	Valves and Appurtenances	20	07-Dec-25	29-Dec-25	01-Feb-26 A	06-Oct-26	$127,197.68	$116,487.63	100%	91.58%
	Valve Rooms	21	25-Dec-25	18-Jan-26	01-Feb-26 A	07-Oct-26	$120,296.07	$99,148.02	100%	82.42%
	Washout Chambers	24	22-Dec-25	18-Jan-26	01-May-26 A	03-Oct-26	$140,613.57	$139,769.89	100%	99.4%
	Air Valve Chambers	20	22-Dec-25	13-Jan-26	22-Mar-26 A	27-Jul-26 A	$94,896.71	$94,896.71	100%	100%
	Flow Meter Chambers	24	22-Dec-25	18-Jan-26	13-Apr-26 A	09-Nov-26	$89,674.62	$36,318.22	100%	40.5%
	Rainwater Collection Ponds Zone 1	309	19-Jan-26	08-Feb-27	22-Jul-25 A	06-Apr-27	36,523,177.3	32,336,788.8	95.14%	88.54%
	Excavation for Rainwater Drainage Pond	37	19-Jan-26	14-Mar-26	22-Jul-25 A	09-Jan-27	$169,132.15	$147,144.97	100%	87%
	General Site Preparation	140	16-Feb-26	20-Aug-26	22-Jul-25 A	16-Jan-27	33,469,057.7	31,108,061.7	100%	92.95%
	Backfilling Works	65	27-Jul-26	12-Oct-26	03-Sep-25 A	28-Jan-27	$361,942.90	$271,457.18	80.75%	75%
	Geotextile & Bedding	66	13-Aug-26	31-Oct-26	07-Jan-26 A	09-Mar-27	$614,117.12	$264,377.42	63.86%	43.05%
	Concrete Structures	45	22-Aug-26	14-Oct-26	01-Mar-26 A	25-Apr-26 A	$442,278.68	$442,278.68	95.56%	100%
	Energy Dissipation & Siphon Structures	42	30-Sep-26	18-Nov-26	01-Oct-25 A	30-Dec-25 A	$101,994.10	$101,994.10	1.4%	100%
	Culvert Structures	71	16-Nov-26	08-Feb-27	03-Feb-26 A	06-Apr-27	1,364,654.5	$1,474.78	0%	0.11%
	Road Crossing Zone 1	183	22-Jun-26	23-Jan-27	08-Apr-27	19-Oct-27	1,655,979.5	$0.00	65.74%	0%
	uPVC Road Crossing Pipes	110	22-Jun-26	29-Oct-26	08-Apr-27	18-Aug-27	1,202,844.7	$0.00	90.5%	0%
	GRP Road Crossing Pipes	87	13-Oct-26	23-Jan-27	03-Aug-27	19-Oct-27	$453,134.81	$0.00	0%	0%
	General	729	19-May-25	18-May-27	19-May-25 A	29-Sep-27	15,097,284.2	9,611,809.5	47.93%	63.67%
	General Items	30	19-May-25	17-Jun-25	19-May-25 A	07-Aug-25 A	$162,229.63	$162,229.63	100%	100%
	Site Setup & Facilities	30	19-May-25	17-Jun-25	19-May-25 A	18-Jun-25 A	$53,699.01	$53,699.01	100%	100%
	Project Laboratory	30	19-May-25	17-Jun-25	18-Jun-25 A	07-Aug-25 A	$108,530.62	$108,530.62	100%	100%
	Local Roads	155	29-Aug-26	16-Mar-27	10-Apr-27	08-Jul-27	$83,955.86	$0.00	0.26%	0%
	Bituminous Construction	103	29-Aug-26	27-Dec-26	10-Apr-27	04-May-27	$73,510.98	$0.00	0.3%	0%
	Precast Curbs (Type K1-D)	52	27-Dec-26	16-Mar-27	04-May-27	08-Jul-27	$10,444.88	$0.00	0%	0%
	Arterial Roads	92	07-May-26	29-Aug-26	27-Jun-26 A	10-Apr-27	$479,616.37	$49,597.05	100%	10.34%
	Earthworks	2	07-May-26	10-May-26	16-Jan-27	18-Jan-27	$16,092.57	$0.00	100%	0%
	Precast Curbs (Type K1-D)	90	10-May-26	29-Aug-26	27-Jun-26 A	10-Apr-27	$463,523.80	$49,597.05	100%	10.7%
	Communications	262	22-Jun-26	18-May-27	04-Nov-25 A	06-May-27	10,712,645.9	9,399,982.8	56.35%	87.75%

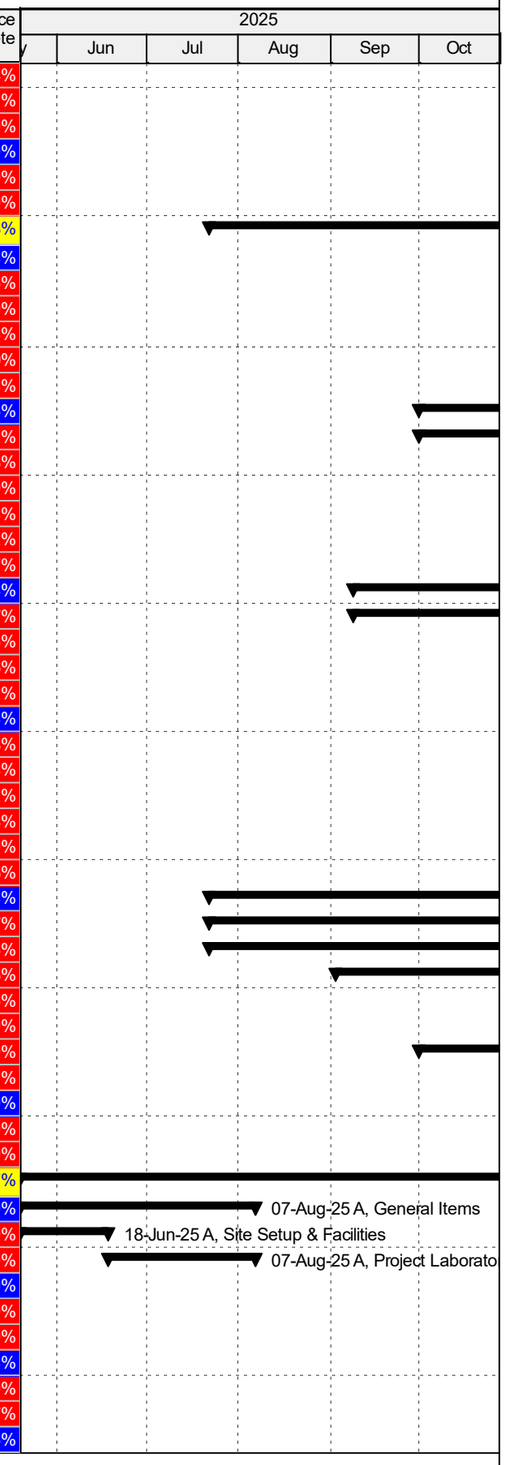

Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary

TASK filter: All Activities

© Oracle Corporation

Development of Phase One – Part Two – Third Industrial

2026 | 2027 | 2028

Nov | Dec | Jan | Feb | Mar | Apr | May | Jun | Jul | Aug | Sep | Oct | Nov | Dec | Jan | Feb | Mar | Apr | May | Jun | Jul | Aug | Sep | Oct | Nov | Dec | Jan

23-Mar-27, Geotextile & Bedding
01-Apr-27, Concrete Structures
15-Jan-26 A, Energy Dissipation & Siphon Structures
02-Aug-27, Road Crossing Zone 2
07-Apr-27, uPVC Road Crossing Pipes
02-Aug-27, GRP Road Crossing Pipes
19-Oct-27, Zone 1
08-Mar-27, Sewerage Network Zone 1
10-Oct-26, Pipework: Supply, Installation, and Testing
05-Nov-26, Fittings and Valves
17-Dec-26, Valve & Flow Meter Chambers
24-Oct-26, Manholes
08-Mar-27, Pumping Stations
02-Nov-26, Rainwater Drainage Network Zone 1
11-Oct-26, Pipe Laying Works
01-Nov-26, Precast Concrete Box Culverts
02-Nov-26, Manholes
10-Oct-26, Chambers and Catch Basins
13-Oct-26, Gully Outfalls to Swales
19-Oct-26, Backfilling & Bedding
29-Nov-26, Potable Water Network Zone 1
04-Oct-26, Pipe Installation Works
06-Oct-26, Valve Installation & Chambers
29-Nov-26, Flow Meter Installation
13-Oct-26, Washout & Air Valve Chambers
09-Nov-26, Irrigation Network Zone 1
03-Oct-26, Excavation, Pipe Laying & Backfilling
06-Oct-26, Valves and Appurtenances
07-Oct-26, Valve Rooms
03-Oct-26, Washout Chambers
27-Jul-26 A, Air Valve Chambers
09-Nov-26, Flow Meter Chambers
06-Apr-27, Rainwater Collection Ponds Zone 1
09-Jan-27, Excavation for Rainwater Drainage Pond
16-Jan-27, General Site Preparation
28-Jan-27, Backfilling Works
09-Mar-27, Geotextile & Bedding
25-Apr-26 A, Concrete Structures
30-Dec-25 A, Energy Dissipation & Siphon Structures
06-Apr-27, Culvert Structures
19-Oct-27, Road Crossing Zone 1
18-Aug-27, uPVC Road Crossing Pipes
19-Oct-27, GRP Road Crossing Pip
29-Sep-27, General
y
08-Jul-27, Local Roads
04-May-27, Bituminous Construction
08-Jul-27, Precast Curbs (Type K1-D)
10-Apr-27, Arterial Roads
18-Jan-27, Earthworks
10-Apr-27, Precast Curbs (Type K1-D)
06-May-27, Communications

Actual Level of Effort | Remaining Work | Milestone
Actual Work | Critical Remaining Work | summary

TASK filter: All Activities

© Oracle Corporation

Development of Phase One – Part Two – Third Industrial

Activity ID	Activity Name	BL Project Duration	BL Project Start	BL Project Finish	Start	Finish	Budgeted Total Cost	Earned Value Cost	Schedule % Complete	Performance % Complete
Ductworks		199	22-Jun-26	14-Feb-27	04-Nov-25 A	18-Apr-27	6,718,317.7	5,623,345.5	89.85%	83.7%
Manholes (Telecom, 2000x1000x1001mm)		63	14-Feb-27	18-May-27	23-Nov-25 A	06-May-27	3,994,328.1	3,776,637.2	0%	94.55%
Landscape		171	29-Jul-26	21-Feb-27	28-Feb-27	29-Sep-27	3,658,836.4	$0.00	15.25%	0%
Supply & Planting of Trees and Shrubs		99	18-Aug-26	13-Dec-26	28-Mar-27	26-Jul-27	1,929,003.8	$0.00	24.43%	0%
Gravel Layer and Bed Preparation		37	29-Jul-26	10-Sep-26	28-Feb-27	20-Apr-27	$86,633.98	$0.00	100%	0%
Landscape Irrigation System		87	05-Nov-26	21-Feb-27	19-Jun-27	29-Sep-27	1,643,198.5	$0.00	0%	0%
Testing & Commissioning & Closeout		382	12-Jan-26	18-May-27	14-Jan-26 A	24-Oct-27	23,377,607.6	12,429,541.4	61.84%	53.17%
Testing & Commissioning		382	12-Jan-26	18-May-27	14-Jan-26 A	11-May-27	23,377,607.6	12,429,541.4	61.84%	53.17%
Zone 3		299	12-Jan-26	19-Jan-27	20-Jan-26 A	11-May-27	5,908,314.1	2,312,989.8	48.94%	39.15%
A102060	Testing and Commissioning for Sewerage Network Zone 3	21	05-Mar-26	09-Apr-26	05-Mar-26 A	20-Dec-26	$350,278.50	$280,222.80	100%	80%
A103590	Testing and Commissioning for Rain Water Drainage Network Zone 3	21	19-Jan-26	11-Feb-26	29-Jan-26 A	01-Dec-26	1,789,001.6	1,431,201.3	100%	80%
A103600	Testing and Commissioning for Potable Water Network Zone 3	21	19-Jan-26	11-Feb-26	31-Jan-26 A	28-Nov-26	$454,067.96	$363,254.36	100%	80%
A103610	Testing and Commissioning for Irrigation Network Zone 3	21	12-Jan-26	04-Feb-26	20-Jan-26 A	13-Dec-26	$297,889.13	$238,311.31	100%	80%
A103620	Testing and Commissioning for Pumping Station Zone 3	21	27-Dec-26	19-Jan-27	17-Apr-27	11-May-27	3,017,076.8	$0.00	0%	0%
Zone 2		57	14-Jan-26	09-Apr-26	14-Jan-26 A	15-Dec-26	5,782,474.4	4,047,732.1	100%	70%
A103640	Testing and Commissioning for Sewerage Network Zone 2	21	05-Mar-26	09-Apr-26	05-Mar-26 A	15-Dec-26	$700,557.00	$490,389.90	100%	70%
A103650	Testing and Commissioning for Rain Water Drainage Network Zone 2	21	19-Jan-26	11-Feb-26	11-Apr-26 A	17-Nov-26	3,578,003.3	2,504,602.3	100%	70%
A103660	Testing and Commissioning for Potable Water Network Zone 2	21	14-Jan-26	07-Feb-26	14-Jan-26 A	02-Dec-26	$908,135.90	$635,695.13	100%	70%
A103670	Testing and Commissioning for Irrigation Network Zone 2	21	19-Jan-26	11-Feb-26	10-Feb-26 A	15-Nov-26	$595,778.27	$417,044.79	100%	70%
Zone 1		296	18-Jan-26	21-Jan-27	18-Jan-26 A	25-Mar-27	8,799,551.3	4,047,732.1	65.71%	46%
A103690	Testing and Commissioning for Sewerage Network Zone 1	21	11-Feb-26	25-Mar-26	11-Feb-26 A	26-Dec-26	$700,557.00	$490,389.90	100%	70%
A103700	Testing and Commissioning for Rain Water Drainage Network Zone 1	21	19-Jan-26	11-Feb-26	19-Jan-26 A	09-Nov-26	3,578,003.3	2,504,602.3	100%	70%
A103710	Testing and Commissioning for Potable Water Network Zone 1	21	18-Jan-26	10-Feb-26	18-Jan-26 A	06-Dec-26	$908,135.90	$635,695.13	100%	70%
A103720	Testing and Commissioning for Irrigation Network Zone 1	21	19-Jan-26	11-Feb-26	19-Jan-26 A	17-Nov-26	$595,778.27	$417,044.79	100%	70%
A103730	Testing and Commissioning for Pumping Station Zone 1	21	29-Dec-26	21-Jan-27	08-Mar-27	25-Mar-27	3,017,076.8	$0.00	0%	0%
General		21	20-Apr-27	18-May-27	14-Jun-26 A	08-May-27	2,887,267.6	2,021,087.3	0%	70%
A103630	Testing and Commissioning for Communication	21	20-Apr-27	18-May-27	14-Jun-26 A	08-May-27	2,887,267.6	2,021,087.3	0%	70%
As-Built		116	12-Dec-26	18-May-27	16-Jan-27	24-Oct-27	$0.00	$0.00	0%	0%
HO-0001	Mechanical as-built Submittals & Approval	21	23-Jan-27	23-Feb-27	11-May-27	09-Jun-27	$0.00	$0.00	0%	0%
HO-13	Earthworks as-built Submittals & Approval	21	12-Dec-26	05-Jan-27	16-Jan-27	10-Feb-27	$0.00	$0.00	0%	0%
HO-23	Roadworks as-built Submittals & Approval	21	16-Mar-27	10-Apr-27	08-Jul-27	02-Aug-27	$0.00	$0.00	0%	0%
HO-3	Electrical as-built Submittals & Approval	21	20-Apr-27	18-May-27	11-May-27	09-Jun-27	$0.00	$0.00	0%	0%
HO-33	Landscape as-built Submittals & Approval	21	23-Feb-27	30-Mar-27	29-Sep-27	24-Oct-27	$0.00	$0.00	0%	0%
Handover		21	20-Apr-27	18-May-27	09-Jun-27	04-Jul-27	$0.00	$0.00	0%	0%
HO-0003	Handover & Demobilization	21	20-Apr-27	18-May-27	09-Jun-27	04-Jul-27	$0.00	$0.00	0%	0%

2025: Jun | Jul | Aug | Sep | Oct

Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary

TASK filter: All Activities

© Oracle Corporation

Development of Phase One – Part Two – Third Industrial

2026: Nov, Dec, Jan, Feb, Mar, Apr, May, Jun, Jul, Aug, Sep, Oct, Nov, Dec
2027: Jan, Feb, Mar, Apr, May, Jun, Jul, Aug, Sep, Oct, Nov, Dec
2028: Jan

18-Apr-27, Ductworks
06-May-27, Manholes (Telecom, 2000x1000x1001mm)
29-Sep-27, Landscape
26-Jul-27, Supply & Planting of Trees and Shrubs
20-Apr-27, Gravel Layer and Bed Preparation
29-Sep-27, Landscape Irrigation System
24-Oct-27, Testing & Commissio
11-May-27, Testing & Commissioning
11-May-27, Zone 3
Testing and Commissioning for Sewerage Network Zone 3
Testing and Commissioning for Rain Water Drainage Network Zone 3
Testing and Commissioning for Potable Water Network Zone 3
Testing and Commissioning for Irrigation Network Zone 3
Testing and Commissioning for Pumping Station Zone 3
15-Dec-26, Zone 2
Testing and Commissioning for Sewerage Network Zone 2
Testing and Commissioning for Rain Water Drainage Network Zone 2
Testing and Commissioning for Potable Water Network Zone 2
Testing and Commissioning for Irrigation Network Zone 2
25-Mar-27, Zone 1
Testing and Commissioning for Sewerage Network Zone 1
Testing and Commissioning for Rain Water Drainage Network Zone 1
Testing and Commissioning for Potable Water Network Zone 1
Testing and Commissioning for Irrigation Network Zone 1
Testing and Commissioning for Pumping Station Zone 1
08-May-27, General
Testing and Commissioning for Communication
24-Oct-27, As-Built
Mechanical as-built Submittals & Approval
Earthworks as-built Submittals & Approval
Roadworks as-built Submittals & Approval
Electrical as-built Submittals & Approval
Landscape as-built Submittals &
04-Jul-27, Handover
Handover & Demobilization

Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary

TASK filter: All Activities

© Oracle Corporation
