
Development of Phase One – Part Two – Third Industrial

Activity ID	Activity Name	Original Duration	BL Project Start	BL Project Finish	Start	Finish	Budgeted Total Cost
Development of Phase One – Part Two – Third Industrial City in Dammam - 01-C		773	19-May-25	18-May-27	19-May-25 A	08-May-27	),382,398.32
Milestones		0	16-Jul-25	16-Jul-25	08-Oct-26	08-Oct-26	$0.00
MIL-0004	Submission and Approval of Drawings and Specifications	0		16-Jul-25		08-Oct-26*	$0.00
Mobilization		463	19-May-25	02-Aug-25	19-May-25 A	10-Dec-26	$0.00
Deliverables		463	19-May-25	02-Aug-25	19-May-25 A	10-Dec-26	$0.00
Submittals		463	19-May-25	02-Aug-25	19-May-25 A	10-Dec-26	$0.00
S100015	Prepare & Submit Pre-commissioning/ Commissioning Plan/ Startup/ Testing / Handover	60	19-May-25	02-Aug-25	03-Oct-26	10-Dec-26	$0.00
S10002	Prepare & Submit Method of Statement	20	19-May-25	16-Jun-25	19-May-25 A	06-Oct-26	$0.00
Approvals		10	17-Jun-25	28-Jun-25	17-Jul-25 A	12-Oct-26	$0.00
S100106	Approval of Method of Statement	10	17-Jun-25	28-Jun-25	17-Jul-25 A	12-Oct-26	$0.00
Engineering		265	03-Jul-25	03-Mar-26	20-Jul-25 A	14-Oct-26	$433,169.77
Shop Drawing		10	03-Jul-25	16-Jul-25	01-Mar-26 A	08-Oct-26	$0.00
Approvals		10	03-Jul-25	16-Jul-25	01-Mar-26 A	08-Oct-26	$0.00
A1630	Landscape details approval	10	03-Jul-25	16-Jul-25	01-Mar-26 A	08-Oct-26	$0.00
Material Submittal & Approval		265	03-Jul-25	03-Mar-26	20-Jul-25 A	14-Oct-26	$433,169.77
Long Lead Items		128	03-Jul-25	30-Jul-25	20-Jul-25 A	07-Oct-26	$311,534.63
Generators & Fuel Tanks - PS & Control Bldg backup power		128	03-Jul-25	30-Jul-25	20-Jul-25 A	07-Oct-26	$311,534.63
A102930	Material Submittal for Generators & Fuel Tanks - PS & Control Bldg backup power	13	03-Jul-25	21-Jul-25	20-Jul-25 A	06-Oct-26	$186,920.78
A102940	Material Approval for Generators & Fuel Tanks - PS & Control Bldg backup power	7	22-Jul-25	30-Jul-25	15-Dec-25 A	07-Oct-26	$124,613.85
Short Lead Items		48	18-Feb-26	03-Mar-26	21-Feb-26 A	14-Oct-26	$121,635.14
Interlock Tiles / Curbstone - Roads, Sidewalks, Landscape		7	18-Feb-26	03-Mar-26	21-Feb-26 A	13-Oct-26	$16,354.74
A103180	Material Approval for Interlock Tiles / Curbstone - Roads, Sidewalks, Landscape	7	18-Feb-26	03-Mar-26	21-Feb-26 A	13-Oct-26	$16,354.74
Landscaping Materials (Soil, Plants) - Final works, softscape		7	18-Feb-26	03-Mar-26	01-Apr-26 A	14-Oct-26	$105,280.40
A103200	Material Approval for Landscaping Materials (Soil, Plants) - Final works, softscape	7	18-Feb-26	03-Mar-26	01-Apr-26 A	14-Oct-26	$105,280.40
Procurement		367	05-Aug-25	25-Jan-27	13-Aug-25 A	16-Jan-27	3,476,564.7
Prequalification		105	19-Jan-26	29-Jan-26	13-Aug-25 A	07-Oct-26	$0.00
Short Lead Items		105	19-Jan-26	29-Jan-26	13-Aug-25 A	07-Oct-26	$0.00
Interlock Tiles / Curbstone - Roads, Sidewalks, Landscape		10	19-Jan-26	29-Jan-26	02-May-26 A	07-Oct-26	$0.00
A103560	Prequalification Approval for Interlock Tiles / Curbstone - Roads, Sidewalks, Landscape	10	19-Jan-26	29-Jan-26	02-May-26 A	07-Oct-26	$0.00
Landscaping Materials (Soil, Plants) - Final works, softscape		10	19-Jan-26	29-Jan-26	13-Aug-25 A	07-Oct-26	$0.00
A103580	Prequalification Approval for Landscaping Materials (Soil, Plants) - Final works, softscape	10	19-Jan-26	29-Jan-26	13-Aug-25 A	07-Oct-26	$0.00
Long Lead Items		181	05-Aug-25	17-Dec-25	08-Dec-25 A	29-Oct-26	2,196,886.8
Control & Instrumentation Devices - Flow meters, pressure sensors		65	04-Oct-25	17-Dec-25	13-Apr-26 A	29-Oct-26	$285,073.41
A102620	Staging Time for Control & Instrumentation Devices - Flow meters, pressure sensors	30	13-Nov-25	17-Dec-25	16-Apr-26 A	29-Oct-26	$0.00
A1570	Delivery for Control & Instrumentation Devices - Flow meters, pressure sensors	35	04-Oct-25	12-Nov-25	13-Apr-26 A	06-Oct-26	$285,073.41
Pumps (Sewage, Irrigation, Booster) - Especially for pumping stations		30	12-Nov-25	16-Dec-25	20-Jan-26 A	07-Oct-26	$0.00
A102640	Staging Time for Pumps (Sewage, Irrigation, Booster) - Especially for pumping stations	30	12-Nov-25	16-Dec-25	20-Jan-26 A	07-Oct-26	$0.00
Generators & Fuel Tanks - PS & Control Bldg backup power		181	05-Aug-25	13-Dec-25	08-Dec-25 A	26-Oct-26	1,911,813.4
A102230	Manufacturing for Generators & Fuel Tanks - PS & Control Bldg backup power	55	05-Aug-25	08-Oct-25	08-Dec-25 A	11-Oct-26	$0.00
A102250	Delivery for Generators & Fuel Tanks - PS & Control Bldg backup power	21	15-Oct-25	08-Nov-25	10-Dec-25 A	12-Oct-26	1,911,813.4
A102670	Custom Clearance for Generators & Fuel Tanks - PS & Control Bldg backup power	5	09-Oct-25	14-Oct-25	01-Jan-26 A	11-Oct-26	$0.00
A102680	Staging Time for Generators & Fuel Tanks - PS & Control Bldg backup power	30	09-Nov-25	13-Dec-25	04-Jul-26 A	26-Oct-26	$0.00
Short Lead Items		271	03-Mar-26	25-Jan-27	24-Nov-25 A	16-Jan-27	1,279,677.8
Asphalt		63	12-Nov-26	25-Jan-27	01-Dec-25 A	01-Dec-26	$635,735.66
A102730	Delivery for Asphalt Phase 1	21	12-Nov-26	07-Dec-26	01-Dec-25 A	01-Dec-26	$211,911.89
A103740	Delivery for Asphalt Phase 2	21	07-Dec-26	31-Dec-26	08-Dec-25 A	01-Dec-26	$211,911.89
A103750	Delivery for Asphalt Phase 3	21	31-Dec-26	25-Jan-27	14-Dec-25 A	01-Dec-26	$211,911.89
Communication Ducts & Manholes - Telecom systems		30	28-Oct-26	02-Dec-26	24-Nov-25 A	16-Jan-27 A	$393,029.41
A102050	Delivery for Communication Ducts & Manholes - Telecom systems	30	28-Oct-26	02-Dec-26	24-Nov-25 A	16-Jan-27 A	$393,029.41

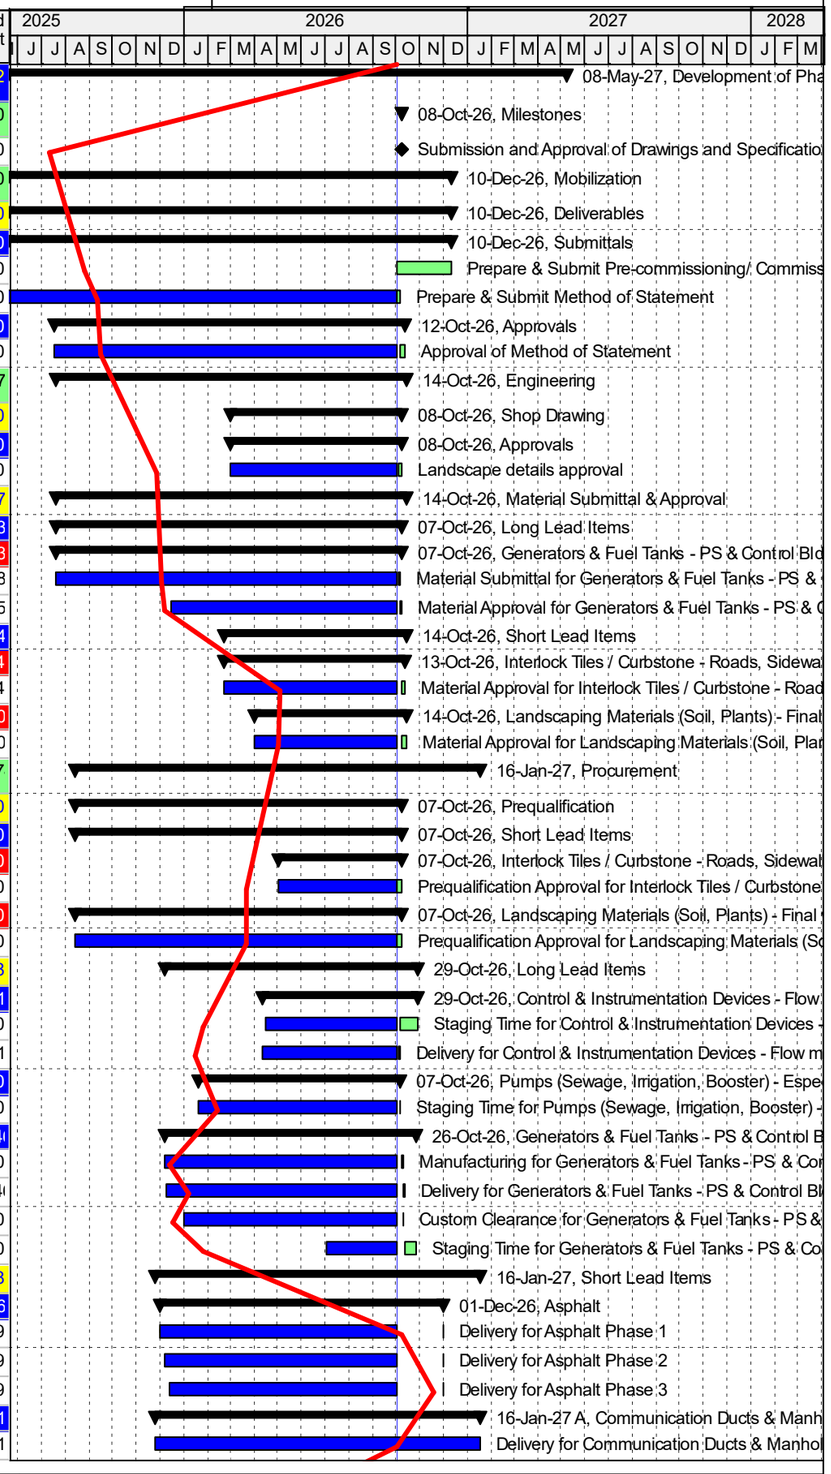


Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary

TASK filter: 2 Weeks Ahead.

© Oracle Corporation

Development of Phase One – Part Two – Third Industrial

Activity ID	Activity Name	Original Duration	BL Project Start	BL Project Finish	Start	Finish	Budgeted Total Cost
Interlock Tiles / Curbstone - Roads, Sidewalks, Landscape		90	11-Mar-26	07-Jul-26	01-Jan-26 A	02-Nov-26	$250,912.80
A102380	Manufacturing for Interlock Tiles / Curbstone - Roads, Sidewalks, Landscape	30	11-Mar-26	23-Apr-26	01-Jan-26 A	13-Oct-26	$0.00
A102400	Delivery for Interlock Tiles / Curbstone - Roads, Sidewalks, Landscape	30	23-Apr-26	02-Jun-26	01-Apr-26 A	14-Oct-26	$250,912.80
A102820	Staging Time for Interlock Tiles / Curbstone - Roads, Sidewalks, Landscape	30	02-Jun-26	07-Jul-26	04-Jul-26 A	02-Nov-26	$0.00
Landscaping Materials (Soil, Plants) - Final works, softscape		64	03-Mar-26	02-Jun-26	14-Oct-26	28-Dec-26	$0.00
A102350	Issue PO for Landscaping Materials (Soil, Plants) - Final works, softscape	4	03-Mar-26	10-Mar-26	14-Oct-26	19-Oct-26	$0.00
A102360	Manufacturing for Landscaping Materials (Soil, Plants) - Final works, softscape	60	11-Mar-26	02-Jun-26	19-Oct-26	28-Dec-26	$0.00
Construction		544	19-Oct-25	25-Apr-27	03-Sep-25 A	18-Apr-27	9,129,209.9
Zone 3		328	19-Oct-25	10-Oct-26	04-Oct-25 A	17-Apr-27	8,851,487.1
Sewerage Network Zone 3		168	19-Oct-25	25-Jun-26	13-Jan-26 A	17-Apr-27	1,439,519.7
Pipework: Supply, Installation, and Testing		147	29-Dec-25	27-Jan-26	01-Mar-26 A	26-Oct-26	$20,836.71
HDPE Pressure Pipes Installation (250mm–630mm)		147	29-Dec-25	27-Jan-26	01-Mar-26 A	26-Oct-26	$20,836.71
MOD-SWN-	Backfilling & Warning Tape HDPE for Sewerage Network Zone 3	15	13-Jan-26	27-Jan-26	12-Oct-26	26-Oct-26	$10,418.36
MOD-SWN-	Coating / Wrapping HDPE for Sewerage Network Zone 3	15	29-Dec-25	12-Jan-26	01-Mar-26 A	11-Oct-26	$10,418.36
Fittings and Valves		24	14-Dec-25	10-Jan-26	03-Oct-26	29-Oct-26	$27,640.08
MOD-SWN-FV-	Supply & Installation of HDPE Elbows for Sewerage Network Zone 3	6	14-Dec-25	20-Dec-25	03-Oct-26	08-Oct-26	$6,826.21
MOD-SWN-FV-	Gate Valves Installation for Sewerage Network Zone 3	4	21-Dec-25	24-Dec-25	10-Oct-26	13-Oct-26	$4,830.30
MOD-SWN-FV-	Drain Valves Installation for Sewerage Network Zone 3	4	25-Dec-25	29-Dec-25	14-Oct-26	18-Oct-26	$4,392.82
MOD-SWN-FV-	Air Breather & Air Release Valves Installation for Sewerage Network Zone 3	10	30-Dec-25	10-Jan-26	19-Oct-26	29-Oct-26	$11,590.74
Valve & Flow Meter Chambers		55	19-Oct-25	06-Jan-26	08-Jun-26 A	09-Nov-26	$33,389.88
Valve Chambers Construction		48	19-Oct-25	20-Dec-25	08-Jun-26 A	01-Nov-26	$5,515.25
MOD-SWN-	Excavation Valve Chamber for Sewerage Network Zone 3	21	19-Oct-25	08-Nov-25	08-Jun-26 A	11-Oct-26	$1,034.11
MOD-SWN-	Lean Concrete / Bedding Valve Chamber for Sewerage Network Zone 3	21	09-Nov-25	29-Nov-25	22-Jul-26 A	21-Oct-26	$689.41
MOD-SWN-	Test Valve Chamber for Sewerage Network Zone 3	15	06-Dec-25	20-Dec-25	04-Aug-26 A	01-Nov-26	$689.41
MOD-SWN-	Valve Chambers Construction Valve Chamber for Sewerage Network Zone 3	6	30-Nov-25	05-Dec-25	31-Jul-26 A	24-Oct-26	$3,102.33
Water Drain Chambers Construction		42	19-Oct-25	24-Dec-25	16-Jun-26 A	03-Nov-26	$15,675.99
MOD-SWN-	Excavation Water Drain Chamber for Sewerage Network Zone 3	21	19-Oct-25	08-Nov-25	16-Jun-26 A	09-Oct-26	$3,359.14
MOD-SWN-	Lean Concrete / Bedding Water Drain Chamber for Sewerage Network Zone 3	21	09-Nov-25	29-Nov-25	23-Jun-26 A	17-Oct-26	$2,239.43
MOD-SWN-	Water Drain Chambers Construction Water Drain Chamber for Sewerage Network Zone 3	19	06-Dec-25	24-Dec-25	01-Jul-26 A	03-Nov-26	$10,077.42
Discharge Chambers Construction		55	19-Oct-25	06-Jan-26	01-Jul-26 A	09-Nov-26	$10,950.53
MOD-SWN-	Excavation Discharge Chamber for Sewerage Network Zone 3	21	19-Oct-25	08-Nov-25	01-Jul-26 A	11-Oct-26	$2,346.54
MOD-SWN-	Lean Concrete / Bedding Discharge Chamber for Sewerage Network Zone 3	21	09-Nov-25	29-Nov-25	15-Jul-26 A	21-Oct-26	$1,564.36
MOD-SWN-	Discharge Chambers Construction Discharge Chamber for Sewerage Network Zone 3	13	25-Dec-25	06-Jan-26	01-Aug-26 A	09-Nov-26	$7,039.63
Flow Meter Chambers Construction		42	19-Oct-25	29-Nov-25	14-Jul-26 A	23-Oct-26	$1,248.11
MOD-SWN-	Excavation Flow Meter Chamber for Sewerage Network Zone 3	21	19-Oct-25	08-Nov-25	14-Jul-26 A	11-Oct-26	$748.87
MOD-SWN-	Lean Concrete / Bedding Flow Meter Chamber for Sewerage Network Zone 3	21	09-Nov-25	29-Nov-25	29-Jul-26 A	23-Oct-26	$499.24
Manholes		59	09-Nov-25	27-Jan-26	24-Feb-26 A	26-Oct-26	$231,760.52
1500mm GRP Manholes (Standard & Backdrop)		42	09-Nov-25	10-Jan-26	10-Mar-26 A	19-Oct-26	$220,145.67
MOD-SWN-	1500mm GRP Manholes (Standard & Backdrop) 1.5m GRP for Sewerage Network Zone	21	21-Dec-25	10-Jan-26	18-Mar-26 A	19-Oct-26	$180,119.19
MOD-SWN-	Lean Concrete / Bedding 1.5m GRP for Sewerage Network Zone 3	21	09-Nov-25	29-Nov-25	10-Mar-26 A	11-Oct-26	$40,026.49
1800mm GRP Manholes (Standard & Backdrop)		59	09-Nov-25	27-Jan-26	24-Feb-26 A	26-Oct-26	$10,982.49
MOD-SWN-	1800mm GRP Manholes (Standard & Backdrop) 1.8m GRP for Sewerage Network Zone	17	11-Jan-26	27-Jan-26	04-Mar-26 A	26-Oct-26	$8,985.68
MOD-SWN-	Lean Concrete / Bedding 1.8m GRP for Sewerage Network Zone 3	21	09-Nov-25	29-Nov-25	24-Feb-26 A	11-Oct-26	$1,996.82
2000mm GRP Manholes (Standard & Backdrop)		21	09-Nov-25	29-Nov-25	04-Mar-26 A	11-Oct-26	$632.35
MOD-SWN-	Lean Concrete / Bedding 2m GRP for Sewerage Network Zone 3	21	09-Nov-25	29-Nov-25	04-Mar-26 A	11-Oct-26	$632.35
Pumping Stations		40	01-Dec-25	25-Jun-26	13-Jan-26 A	17-Apr-27	1,125,892.5
In-Line Booster Stations		21	01-Dec-25	24-Dec-25	03-Oct-26	26-Oct-26	$656,073.36
MOD-SWN-	In-Line Booster Stations - Civil Works for Sewerage Network Zone 3	21	01-Dec-25	24-Dec-25	03-Oct-26	26-Oct-26	$656,073.36
Engine/Motor Control Center Buildings		7	01-Dec-25	08-Dec-25	04-Oct-26	11-Oct-26	$42,052.73
MOD-SWN-	MCC Building – PS4 for Sewerage Network Zone 3	7	01-Dec-25	08-Dec-25	04-Oct-26	11-Oct-26	$42,052.73

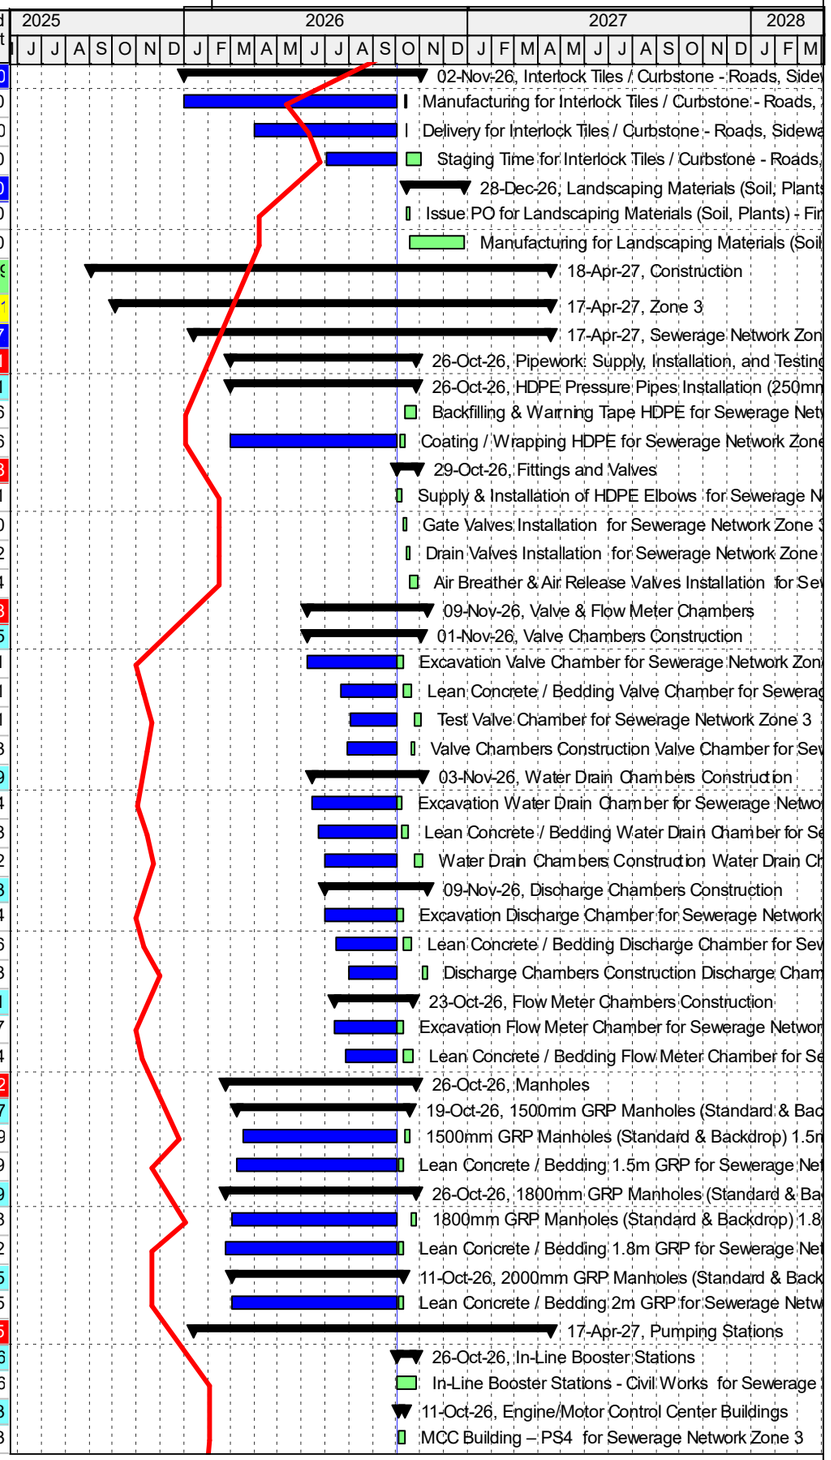


Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary

TASK filter: 2 Weeks Ahead.

© Oracle Corporation

Development of Phase One – Part Two – Third Industrial

Activity ID	Activity Name	Original Duration	BL Project Start	BL Project Finish	Start	Finish	Budgeted Total Cost
Valves and Fittings (General Supply & Installation)		8	18-Dec-25	27-Dec-25	30-Aug-26 A	05-Nov-26	$43,723.31
MOD-SWN-	Valves, fittings, flow meters – PS3 for Sewerage Network Zone 3	2	18-Dec-25	20-Dec-25	30-Aug-26 A	31-Oct-26	$11,924.59
MOD-SWN-	Valves, fittings, flow meters – PS4 for Sewerage Network Zone 3	3	21-Dec-25	23-Dec-25	01-Sep-26 A	03-Nov-26	$14,516.89
MOD-SWN-	35mm SS 316 mesh network – PS4 for Sewerage Network Zone 3	3	24-Dec-25	27-Dec-25	08-Sep-26 A	05-Nov-26	$17,281.83
Lighting Works		13	10-Jun-26	25-Jun-26	13-Jan-26 A	17-Apr-27	$384,043.12
MOD-SWN-	250W Flood Light installation – PS3 & PS4 for Sewerage Network Zone 3	13	10-Jun-26	25-Jun-26	13-Jan-26 A	17-Apr-27	$384,043.12
Rainwater Drainage Network Zone 3		215	15-Nov-25	18-Jan-26	05-Jan-26 A	31-Oct-26	3,861,084.2
Pipe Laying Works		214	03-Dec-25	18-Jan-26	05-Jan-26 A	30-Oct-26	$154,441.32
Supply & Installation of uPVC Pipes (250–300mm dia)		82	06-Dec-25	13-Dec-25	23-Feb-26 A	09-Oct-26	$75,388.93
MOD-RWN-	Coating / Wrapping UPVC for Rainwater Drainage Network Zone 3	2	06-Dec-25	07-Dec-25	23-Feb-26 A	06-Oct-26	$37,694.46
MOD-RWN-	Backfilling & Warning Tape UPVC for Rainwater Drainage Network Zone 3	8	06-Dec-25	13-Dec-25	21-Jun-26 A	09-Oct-26	$37,694.46
Supply & Installation of GRP Pipes (350–800mm dia)		42	08-Dec-25	18-Jan-26	01-Jun-26 A	23-Oct-26	$51,668.82
MOD-RWN-	Test (Pressure-slope) GRP for Rainwater Drainage Network Zone 3	11	08-Dec-25	18-Dec-25	01-Jun-26 A	08-Oct-26	$17,222.94
MOD-RWN-	Coating / Wrapping GRP for Rainwater Drainage Network Zone 3	21	19-Dec-25	08-Jan-26	01-Jul-26 A	18-Oct-26	$17,222.94
MOD-RWN-	Backfilling & compaction GRP for Rainwater Drainage Network Zone 3	10	09-Jan-26	18-Jan-26	01-Aug-26 A	23-Oct-26	$17,222.94
uPVC Connection Pipes (150mm dia)		214	03-Dec-25	03-Jan-26	05-Jan-26 A	30-Oct-26	$27,383.57
MOD-RWN-	Lay & connect UPVC Con. for Rainwater Drainage Network Zone 3	8	03-Dec-25	10-Dec-25	05-Jan-26 A	06-Oct-26	$18,957.86
MOD-RWN-	Test (Pressure-slope) UPVC Con. for Rainwater Drainage Network Zone 3	3	11-Dec-25	13-Dec-25	06-Oct-26	09-Oct-26	$4,212.86
MOD-RWN-	Coating / Wrapping UPVC Con. for Rainwater Drainage Network Zone 3	21	14-Dec-25	03-Jan-26	09-Oct-26	30-Oct-26	$4,212.86
Precast Concrete Box Culverts		45	15-Nov-25	18-Dec-25	05-Sep-26 A	27-Oct-26	$609,520.19
Box Culverts (500x500mm to 3500x800mm)		45	15-Nov-25	18-Dec-25	05-Sep-26 A	27-Oct-26	$609,520.19
MOD-RWN-	Dewatering and trench shoring Box culvert for Rainwater Drainage Network Zone 3	10	15-Nov-25	02-Dec-25	05-Sep-26 A	11-Oct-26	$212,007.02
MOD-RWN-	Bedding preparation (gravel/lean concrete) Box culvert for Rainwater Drainage Network Z	4	02-Dec-25	07-Dec-25	11-Oct-26	15-Oct-26	$79,502.63
MOD-RWN-	Installation of box culvert units Box culvert for Rainwater Drainage Network Zone 3	10	07-Dec-25	18-Dec-25	15-Oct-26	27-Oct-26	$318,010.53
Manholes		7	07-Dec-25	15-Dec-25	15-Oct-26	24-Oct-26	$27,301.33
Circular GRP Manholes (1200–1800mm dia)		7	07-Dec-25	15-Dec-25	15-Oct-26	24-Oct-26	$8,004.81
MOD-RWN-	Excavate to full manhole depth Circular Manhole for Rainwater Drainage Network Zone 3	7	07-Dec-25	15-Dec-25	15-Oct-26	24-Oct-26	$8,004.81
Concrete Manholes for 1500x1500 Box Pipes		6	07-Dec-25	14-Dec-25	15-Oct-26	22-Oct-26	$12,407.65
MOD-RWN-	Excavation Concrete Manhole 1.5x1.5 for Rainwater Drainage Network Zone 3	6	07-Dec-25	14-Dec-25	15-Oct-26	22-Oct-26	$12,407.65
Concrete Manholes for 1000x1000 Box Pipes		6	07-Dec-25	14-Dec-25	15-Oct-26	22-Oct-26	$6,888.88
MOD-RWN-	Excavation Concrete Manhole 1x1 for Rainwater Drainage Network Zone 3	6	07-Dec-25	14-Dec-25	15-Oct-26	22-Oct-26	$6,888.88
Chambers and Catch Basins		114	29-Dec-25	17-Jan-26	16-Mar-26 A	21-Oct-26	$74,226.71
Gully Outfalls		33	29-Dec-25	05-Jan-26	16-Mar-26 A	17-Oct-26	$31,336.47
MOD-RWN-	Provide slope protection (riprap) Gully Outfall for Rainwater Drainage Network Zone 3	4	29-Dec-25	03-Jan-26	16-Mar-26 A	15-Oct-26	$13,429.92
MOD-RWN-	Compact and shape terrain Gully Outfall for Rainwater Drainage Network Zone 3	2	03-Jan-26	05-Jan-26	23-Jun-26 A	17-Oct-26	$17,906.55
Rainwater Catch Basins		2	07-Jan-26	10-Jan-26	01-Jul-26 A	15-Oct-26	$26,080.25
MOD-RWN-	Backfill and surface finish Catch Basin for Rainwater Drainage Network Zone 3	2	07-Jan-26	10-Jan-26	01-Jul-26 A	15-Oct-26	$26,080.25
Precast Chambers for Absorption Pits		5	11-Jan-26	17-Jan-26	15-Oct-26	21-Oct-26	$16,809.98
MOD-RWN-	Backfill and compact Absorption Pit for Rainwater Drainage Network Zone 3	5	11-Jan-26	17-Jan-26	15-Oct-26	21-Oct-26	$16,809.98
Gully Outfalls to Swales		136	28-Dec-25	17-Jan-26	09-Feb-26 A	31-Oct-26	$150,363.53
Gully Outfalls to Swales		127	31-Dec-25	17-Jan-26	09-Feb-26 A	20-Oct-26	$127,366.76
MOD-RWN-	Excavate outfall channel Gully Outfall to Swales for Rainwater Drainage Network Zone 3	4	31-Dec-25	05-Jan-26	09-Feb-26 A	15-Oct-26	$28,303.72
MOD-RWN-	Place concrete apron or pipes Gully Outfall to Swales for Rainwater Drainage Network Zc	5	05-Jan-26	11-Jan-26	01-Mar-26 A	17-Oct-26	$63,683.38
MOD-RWN-	Provide slope protection (riprap) Gully Outfall to Swales for Rainwater Drainage Network Z	3	11-Jan-26	14-Jan-26	04-Mar-26 A	18-Oct-26	$21,227.79
MOD-RWN-	Compact and shape terrain Gully Outfall to Swales for Rainwater Drainage Network Zone	2	14-Jan-26	17-Jan-26	18-Oct-26	20-Oct-26	$14,151.86
Riprap Works & Protection		13	28-Dec-25	12-Jan-26	15-Oct-26	31-Oct-26	$22,996.78
MOD-RWN-	Lay filter fabric/membrane for Rainwater Drainage Network Zone 3	3	28-Dec-25	31-Dec-25	15-Oct-26	19-Oct-26	$3,537.97
MOD-RWN-	Place riprap/stone layer for Rainwater Drainage Network Zone 3	10	31-Dec-25	12-Jan-26	19-Oct-26	31-Oct-26	$19,458.81
Backfilling & Bedding		120	03-Dec-25	18-Jan-26	29-Mar-26 A	26-Oct-26	$535,371.75
Gravel Bedding & Filter Cloth for uPVC Drain Pipes		120	03-Dec-25	18-Jan-26	29-Mar-26 A	26-Oct-26	$535,371.75
MOD-RWN-	Lay pipe within gravel zone for Rainwater Drainage Network Zone 3	21	03-Dec-25	28-Dec-25	29-Mar-26 A	06-Oct-26	$344,167.55

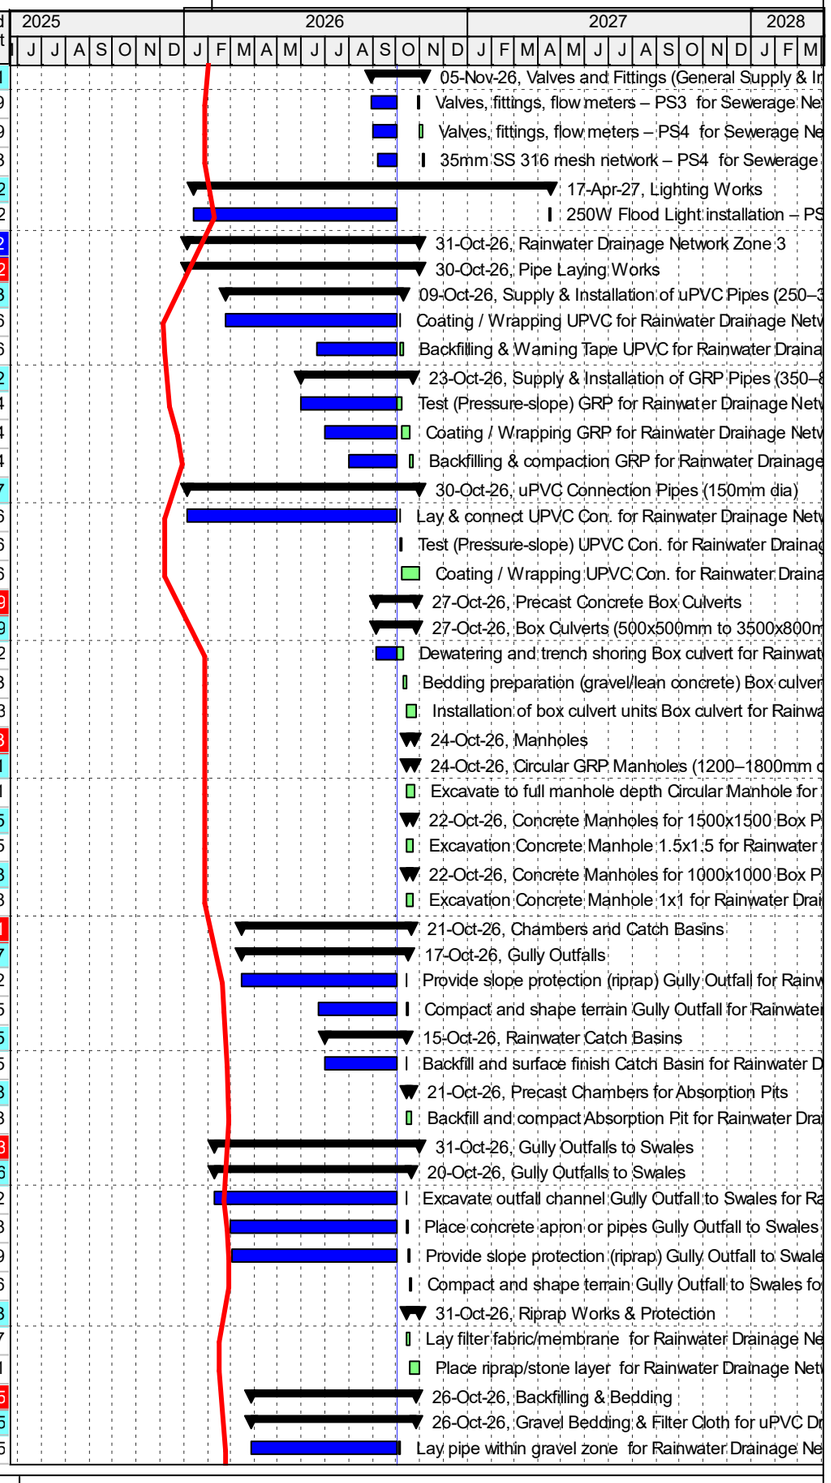


Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary

TASK filter: 2 Weeks Ahead.

© Oracle Corporation

Development of Phase One – Part Two – Third Industrial

Activity ID	Activity Name	Original Duration	BL Project Start	BL Project Finish	Start	Finish	Budgeted Total Cost
MOD-RWN-	Wrap filter cloth above pipe for Rainwater Drainage Network Zone 3	6	28-Dec-25	04-Jan-26	01-Jul-26 A	12-Oct-26	$114,722.52
MOD-RWN-	Final fill and trench restoration for Rainwater Drainage Network Zone 3	12	04-Jan-26	18-Jan-26	12-Oct-26	26-Oct-26	$76,481.68
Deep Basin for Groundwater Collection (2.5–3.0m)		136	30-Nov-25	18-Jan-26	16-Feb-26 A	26-Oct-26	2,309,859.4
MOD-RWN-DB	Pipe connections for inflow for Rainwater Drainage Network Zone 3	12	30-Nov-25	14-Dec-25	16-Feb-26 A	06-Oct-26	$513,302.09
MOD-RWN-DB	Cover slab and access shaft for Rainwater Drainage Network Zone 3	13	14-Dec-25	29-Dec-25	24-Feb-26 A	10-Oct-26	$769,953.14
MOD-RWN-DB	Waterproofing & sealant for Rainwater Drainage Network Zone 3	10	29-Dec-25	10-Jan-26	04-Jul-26 A	18-Oct-26	$898,278.67
MOD-RWN-DB	Backfill in controlled layers for Rainwater Drainage Network Zone 3	7	10-Jan-26	18-Jan-26	18-Oct-26	26-Oct-26	$128,325.52
Potable Water Network Zone 3		269	19-Oct-25	18-Jan-26	13-Oct-25 A	22-Dec-26	6,706,347.8
Pipe Installation Works		68	13-Nov-25	14-Dec-25	16-Jan-26 A	13-Oct-26	$751,774.60
MOD-PWN-PI-	HDPE Pipe Laying (200 mm to 710 mm) for Potable Water Network Zone 3	10	13-Nov-25	03-Dec-25	16-Jan-26 A	08-Oct-26	$451,064.76
MOD-PWN-PI-	Test (Pressure-slope) for Potable Water Network Zone 3	3	04-Dec-25	06-Dec-25	01-Feb-26 A	09-Oct-26	$100,236.61
MOD-PWN-PI-	Coating / Wrapping for Potable Water Network Zone 3	5	07-Dec-25	11-Dec-25	09-Feb-26 A	11-Oct-26	$100,236.61
MOD-PWN-PI-	Backfilling & Warning Tape for Potable Water Network Zone 3	3	12-Dec-25	14-Dec-25	23-Feb-26 A	13-Oct-26	$100,236.61
Valve Installation & Chambers		14	27-Dec-25	11-Jan-26	04-Oct-26	20-Oct-26	$31,630.34
MOD-PWN-VC	Fixing Covers, Gratings, Frames for Potable Water Network Zone 3	14	27-Dec-25	11-Jan-26	04-Oct-26	20-Oct-26	$31,630.34
Flow Meter Installation		8	30-Nov-25	08-Dec-25	05-Sep-26 A	10-Oct-26	$9,230.42
MOD-PWN-FM	RC or Precast Chamber Construction for Potable Water Network Zone 3	8	30-Nov-25	08-Dec-25	05-Sep-26 A	10-Oct-26	$9,230.42
Washout & Air Valve Chambers		34	20-Nov-25	03-Jan-26	08-Aug-26 A	12-Oct-26	$236,386.93
MOD-PWN-W/	Washout (Valve + Outlet) Installation for Potable Water Network Zone 3	8	08-Dec-25	16-Dec-25	16-Aug-26 A	07-Oct-26	$64,769.25
MOD-PWN-W/	Air Valve Rooms (Valve + Outlet) Installation for Potable Water Network Zone 3	6	22-Dec-25	28-Dec-25	16-Aug-26 A	10-Oct-26	$45,075.10
MOD-PWN-W/	Covers, Ladders & Tags for Potable Water Network Zone 3	3	29-Dec-25	31-Dec-25	15-Sep-26 A	10-Oct-26	$19,468.09
MOD-PWN-W/	Backfilling & Final Finishing for Potable Water Network Zone 3	2	01-Jan-26	03-Jan-26	10-Oct-26	12-Oct-26	$19,468.09
MOD-PWN-W/	Pipe Work for Potable Water Network Zone 3	15	20-Nov-25	07-Dec-25	08-Aug-26 A	06-Oct-26	$87,606.40
Pumping Station (Structure & Civil Works)		18	19-Oct-25	09-Nov-25	03-Oct-26	22-Oct-26	$157,715.02
MOD-PWN-PS	Excavation & Blinding for Potable Water Network Zone 3	10	19-Oct-25	30-Oct-25	03-Oct-26	13-Oct-26	$78,857.51
MOD-PWN-PS	Reinforced Concrete/GRP Shell Construction for Potable Water Network Zone 3	8	30-Oct-25	09-Nov-25	14-Oct-26	22-Oct-26	$78,857.51
Water Storage System		11	05-Jan-26	18-Jan-26	13-Oct-25 A	22-Dec-26	5,159,570.0
MOD-PWN-WS	Structural tanks for supply or pressure equalization for Potable Water Network Zone 3	11	05-Jan-26	18-Jan-26	13-Oct-25 A	22-Dec-26	5,159,570.0
Street Lighting		16	22-Dec-25	11-Jan-26	13-Dec-25 A	30-Nov-26	$360,040.43
MOD-PWN-SL-	Conduits, Cabling, Backfilling for Potable Water Network Zone 3	12	22-Dec-25	05-Jan-26	15-Dec-25 A	30-Nov-26	$72,008.09
MOD-PWN-SL-	Pole & Fixture Installation for Potable Water Network Zone 3	16	24-Dec-25	11-Jan-26	13-Dec-25 A	30-Nov-26	$288,032.34
Irrigation Network Zone 3		128	18-Nov-25	30-Dec-25	07-Apr-26 A	03-Nov-26	$434,357.99
Excavation, Pipe Laying & Backfilling		128	18-Nov-25	14-Dec-25	07-Apr-26 A	09-Oct-26	$409,713.37
MOD-IRN-EB-1	HDPE Pipe Laying (125 mm to 630 mm) for Irrigation Network Zone 3	21	18-Nov-25	08-Dec-25	07-Apr-26 A	08-Oct-26	$245,828.02
MOD-IRN-EB-1	Test (Pressure-slope) for Irrigation Network Zone 3	2	09-Dec-25	10-Dec-25	01-May-26 A	08-Oct-26	$54,628.45
MOD-IRN-EB-1	Coating / Wrapping for Irrigation Network Zone 3	2	11-Dec-25	12-Dec-25	01-Jun-26 A	08-Oct-26	$54,628.45
MOD-IRN-EB-1	Backfilling & Warning Tape for Irrigation Network Zone 3	2	13-Dec-25	14-Dec-25	13-Jul-26 A	09-Oct-26	$54,628.45
Valves and Appurtenances		2	27-Dec-25	28-Dec-25	07-Jul-26 A	06-Oct-26	$2,225.96
MOD-IRN-VA-9	Support Brackets/Anchor Blocks for Irrigation Network Zone 3	2	27-Dec-25	28-Dec-25	07-Jul-26 A	06-Oct-26	$2,225.96
Flow Meter Chambers		9	18-Dec-25	30-Dec-25	01-Jul-26 A	03-Nov-26	$22,418.66
MOD-IRN-FC-8	Flow Meter Installation (280, 300, 500 mm) Flow Meter Chamber for Irrigation Network Z	6	18-Dec-25	24-Dec-25	01-Jul-26 A	01-Nov-26	$15,693.06
MOD-IRN-FC-9	Integration with Pipework Flow Meter Chamber for Irrigation Network Zone 3	5	25-Dec-25	30-Dec-25	02-Jul-26 A	03-Nov-26	$6,725.60
Rainwater Collection Ponds Zone 3		206	22-Jan-26	10-Oct-26	04-Oct-25 A	16-Jan-27	16,019,252.8
Excavation for Rainwater Drainage Pond		186	22-Jan-26	10-Mar-26	04-Oct-25 A	06-Jan-27	$374,909.60
Deep excavation, backfill, disposal for pond formation		186	22-Jan-26	10-Mar-26	04-Oct-25 A	06-Jan-27	$374,909.60
MOD-RCP-E	Place warning tapes for Rainwater Collection Ponds Zone 3	6	11-Feb-26	19-Feb-26	01-Jul-26 A	04-Jan-27	$29,598.13
MOD-RCP-E	Dispose of rock/materials to approved dump area for Rainwater Collection Ponds Zone 3	7	19-Feb-26	05-Mar-26	10-Aug-26 A	06-Jan-27	$98,660.42
MOD-RCP-E	Backfill selected areas as per design for Rainwater Collection Ponds Zone 3	2	07-Mar-26	10-Mar-26	01-Sep-26 A	06-Jan-27	$7,892.83
MOD-RCP-E	Excavate in layers to final depth for Rainwater Collection Ponds Zone 3	12	22-Jan-26	04-Feb-26	04-Oct-25 A	02-Jan-27	$120,365.71
MOD-RCP-E	Dewater during excavation for Rainwater Collection Ponds Zone 3	5	05-Feb-26	10-Feb-26	01-Mar-26 A	03-Jan-27	$118,392.51

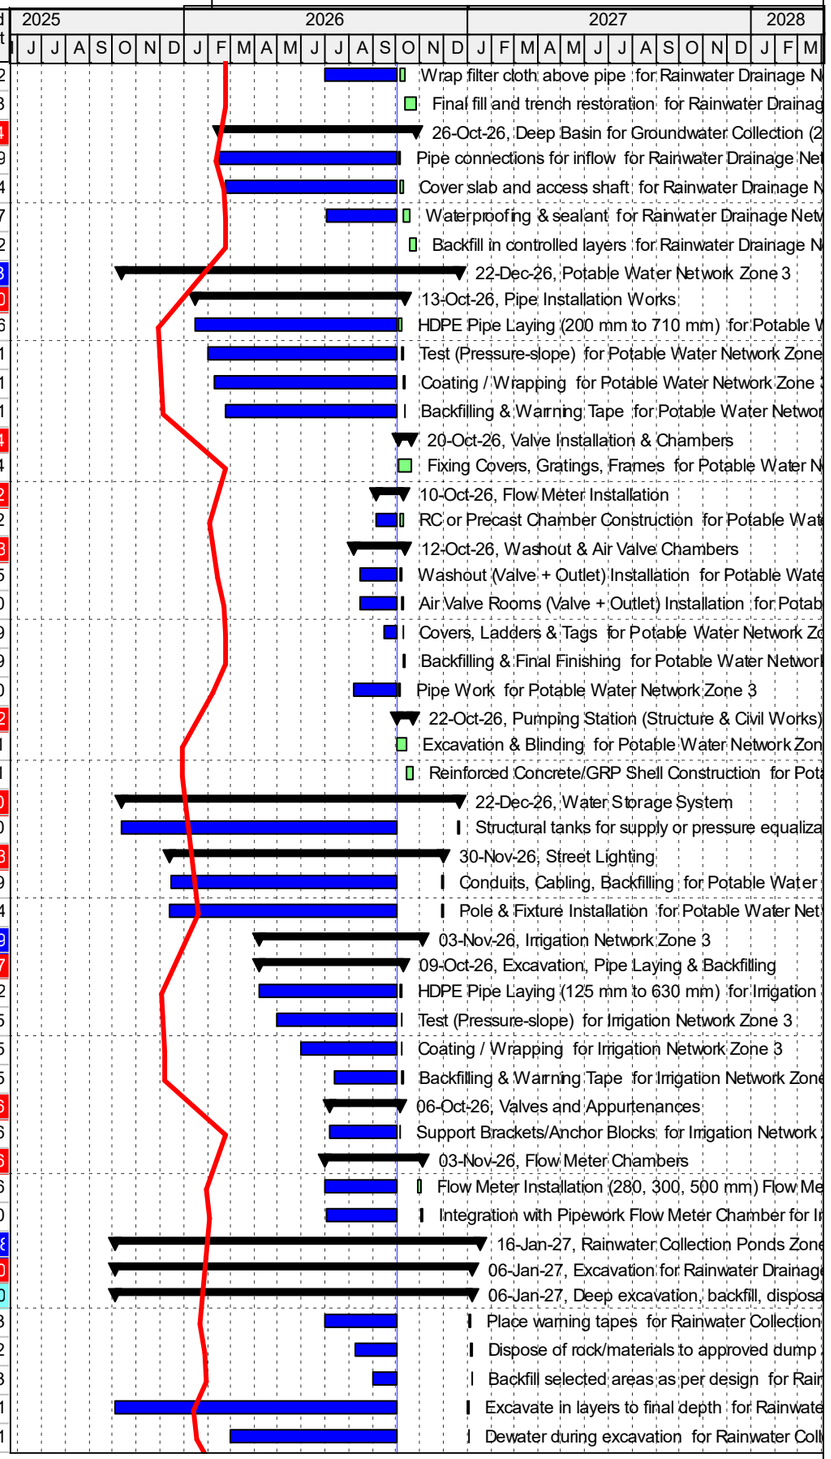


Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary

TASK filter: 2 Weeks Ahead.

© Oracle Corporation

Development of Phase One – Part Two – Third Industrial

Activity ID	Activity Name	Original Duration	BL Project Start	BL Project Finish	Start	Finish	Budgeted Total Cost
General Site Preparation		39	16-Mar-26	10-May-26	12-Oct-25 A	05-Jan-27	4,165,976.4
MOD-RCP-GS-	Earthwork excavation (other than topsoil or rock) - Zone 3 (3 Ponds) for Rainwater Collec	21	16-Mar-26	15-Apr-26	12-Oct-25 A	03-Jan-27	7,689,673.8
MOD-RCP-GS-	Transport and disposal to approved locations - Zone 3 (3 Ponds) for Rainwater Collectio	21	15-Apr-26	10-May-26	06-Dec-25 A	05-Jan-27	6,476,302.5
Backfilling Works		146	10-May-26	23-Jul-26	18-Nov-25 A	16-Jan-27	$802,306.77
MOD-RCP-BW	Select material from excavation or import approved material for Rainwater Collection Po	15	10-May-26	01-Jun-26	11-Dec-25 A	07-Jan-27	$168,906.69
MOD-RCP-BW	Place in layers not exceeding 300mm for Rainwater Collection Ponds Zone 3	21	01-Jun-26	25-Jun-26	29-Nov-25 A	10-Jan-27	$295,586.71
MOD-RCP-BW	Compact each layer to required density for Rainwater Collection Ponds Zone 3	20	25-Jun-26	19-Jul-26	18-Nov-25 A	14-Jan-27	$211,133.36
MOD-RCP-BW	Conduct field density tests for Rainwater Collection Ponds Zone 3	4	19-Jul-26	23-Jul-26	01-Aug-26 A	16-Jan-27	$126,680.02
Geotextile & Bedding		28	01-Jun-26	04-Jul-26	12-Jan-26 A	16-Jan-27	$644,822.98
Installation of geotextile lining and coarse sand bedding		28	01-Jun-26	04-Jul-26	12-Jan-26 A	16-Jan-27	$644,822.98
MOD-RCP-C	Trim subgrade to required level for Rainwater Collection Ponds Zone 3	7	01-Jun-26	09-Jun-26	12-Jan-26 A	09-Jan-27	$143,293.99
MOD-RCP-C	Lay HDPE geotextile membrane over compacted soil for Rainwater Collection Ponds Zo	21	09-Jun-26	04-Jul-26	29-Jan-26 A	16-Jan-27	$501,528.98
Concrete Structures		7	01-Oct-26	10-Oct-26	16-May-26 A	26-Nov-26 A	$22,907.54
Construction of pond slab, walls, vertical structures		7	01-Oct-26	10-Oct-26	16-May-26 A	26-Nov-26 A	$22,907.54
MOD-RCP-C	Apply waterproofing, bitumen, screed, perimeter lining for Rainwater Collection Ponds Z	7	01-Oct-26	10-Oct-26	16-May-26 A	26-Nov-26 A	$22,907.54
Energy Dissipation & Siphon Structures		3	26-Sep-26	29-Sep-26	18-Nov-25 A	01-Dec-26 A	$8,329.52
Siphon pipes, energy dissipators, and associated civil works		3	26-Sep-26	29-Sep-26	18-Nov-25 A	01-Dec-26 A	$8,329.52
MOD-RCP-E	Excavate for low-level areas for Rainwater Collection Ponds Zone 3	3	26-Sep-26	29-Sep-26	18-Nov-25 A	01-Dec-26 A	$8,329.52
Road Crossing Zone 3		24	12-Feb-26	07-May-26	01-Apr-26 A	16-Jan-27	$390,924.54
uPVC Road Crossing Pipes		24	12-Feb-26	07-May-26	01-Apr-26 A	16-Jan-27	$390,924.54
Installation of uPVC pipes of various diameters crossing roadways		24	12-Feb-26	07-May-26	01-Apr-26 A	16-Jan-27	$390,924.54
MOD-ROC-F	Excavation across road width to required depth for Road Crossing Zone 3	10	12-Feb-26	26-Mar-26	09-Jun-26 A	05-Jan-27	$90,213.36
MOD-ROC-F	Preparation of trench base with compacted bedding for Road Crossing Zone 3	10	26-Mar-26	13-Apr-26	01-Apr-26 A	10-Jan-27	$60,142.24
MOD-ROC-F	Laying of uPVC pipe (300mm, 315mm, 400mm, 600mm dia) for Road Crossing Zone 3	10	13-Apr-26	07-May-26	01-May-26 A	16-Jan-27	$240,568.95
Zone 2		338	19-Oct-25	27-Sep-26	17-Nov-25 A	01-Apr-27	6,546,108.4
Sewerage Network Zone 2		306	19-Oct-25	17-Feb-26	11-Jan-26 A	10-Nov-26	1,358,251.5
Pipework: Supply, Installation, and Testing		157	19-Oct-25	19-Jan-26	11-Jan-26 A	10-Nov-26	$187,530.42
HDPE Pressure Pipes Installation (250mm–630mm)		157	19-Oct-25	19-Jan-26	11-Jan-26 A	10-Nov-26	$187,530.42
MOD-SWN-	HDPE Pressure Pipes Installation (250mm–630mm) HDPE for Sewerage Network Zone 2	21	30-Nov-25	20-Dec-25	09-Feb-26 A	26-Oct-26	$93,765.21
MOD-SWN-	Excavation and Trenching HDPE for Sewerage Network Zone 2	21	19-Oct-25	08-Nov-25	11-Jan-26 A	07-Oct-26	$41,673.43
MOD-SWN-	Lean Concrete / Bedding HDPE for Sewerage Network Zone 2	21	09-Nov-25	29-Nov-25	15-Jan-26 A	15-Oct-26	$10,418.36
MOD-SWN-	Test (Pressure - Slope) HDPE for Sewerage Network Zone 2	15	21-Dec-25	04-Jan-26	16-Mar-26 A	02-Nov-26	$20,836.71
MOD-SWN-	Coating / Wrapping HDPE for Sewerage Network Zone 2	15	05-Jan-26	19-Jan-26	21-Mar-26 A	10-Nov-26	$20,836.71
Valve & Flow Meter Chambers		134	19-Oct-25	06-Jan-26	01-Jul-26 A	03-Nov-26	$66,779.77
Valve Chambers Construction		115	19-Oct-25	20-Dec-25	01-Jul-26 A	02-Nov-26	$11,030.50
MOD-SWN-	Excavation Valve Chamber for Sewerage Network Zone 2	21	19-Oct-25	08-Nov-25	01-Jul-26 A	07-Oct-26	$2,068.22
MOD-SWN-	Lean Concrete / Bedding Valve Chamber for Sewerage Network Zone 2	21	09-Nov-25	29-Nov-25	14-Jul-26 A	15-Oct-26	$1,378.81
MOD-SWN-	Test Valve Chamber for Sewerage Network Zone 2	15	06-Dec-25	20-Dec-25	18-Oct-26	02-Nov-26	$1,378.81
MOD-SWN-	Valve Chambers Construction Valve Chamber for Sewerage Network Zone 2	6	30-Nov-25	05-Dec-25	28-Jul-26 A	18-Oct-26	$6,204.65
Water Drain Chambers Construction		67	19-Oct-25	24-Dec-25	28-Jul-26 A	28-Oct-26	$31,351.99
MOD-SWN-	Excavation Water Drain Chamber for Sewerage Network Zone 2	21	19-Oct-25	08-Nov-25	28-Jul-26 A	07-Oct-26	$6,718.28
MOD-SWN-	Lean Concrete / Bedding Water Drain Chamber for Sewerage Network Zone 2	21	09-Nov-25	29-Nov-25	01-Aug-26 A	15-Oct-26	$4,478.86
MOD-SWN-	Water Drain Chambers Construction Water Drain Chamber for Sewerage Network Zone 2	19	06-Dec-25	24-Dec-25	18-Aug-26 A	28-Oct-26	$20,154.85
Discharge Chambers Construction		45	19-Oct-25	06-Jan-26	14-Jul-26 A	03-Nov-26	$21,901.06
MOD-SWN-	Excavation Discharge Chamber for Sewerage Network Zone 2	21	19-Oct-25	08-Nov-25	14-Jul-26 A	11-Oct-26	$4,693.08
MOD-SWN-	Lean Concrete / Bedding Discharge Chamber for Sewerage Network Zone 2	21	09-Nov-25	29-Nov-25	17-Aug-26 A	21-Oct-26	$3,128.72
MOD-SWN-	Discharge Chambers Construction Discharge Chamber for Sewerage Network Zone 2	13	25-Dec-25	06-Jan-26	18-Aug-26 A	03-Nov-26	$14,079.25
Flow Meter Chambers Construction		42	19-Oct-25	29-Nov-25	19-Aug-26 A	23-Oct-26	$2,496.22
MOD-SWN-	Excavation Flow Meter Chamber for Sewerage Network Zone 2	21	19-Oct-25	08-Nov-25	19-Aug-26 A	11-Oct-26	$1,497.73
MOD-SWN-	Lean Concrete / Bedding Flow Meter Chamber for Sewerage Network Zone 2	21	09-Nov-25	29-Nov-25	26-Aug-26 A	23-Oct-26	$998.49
Manholes		230	09-Nov-25	17-Feb-26	07-Feb-26 A	30-Oct-26	1,103,941.3

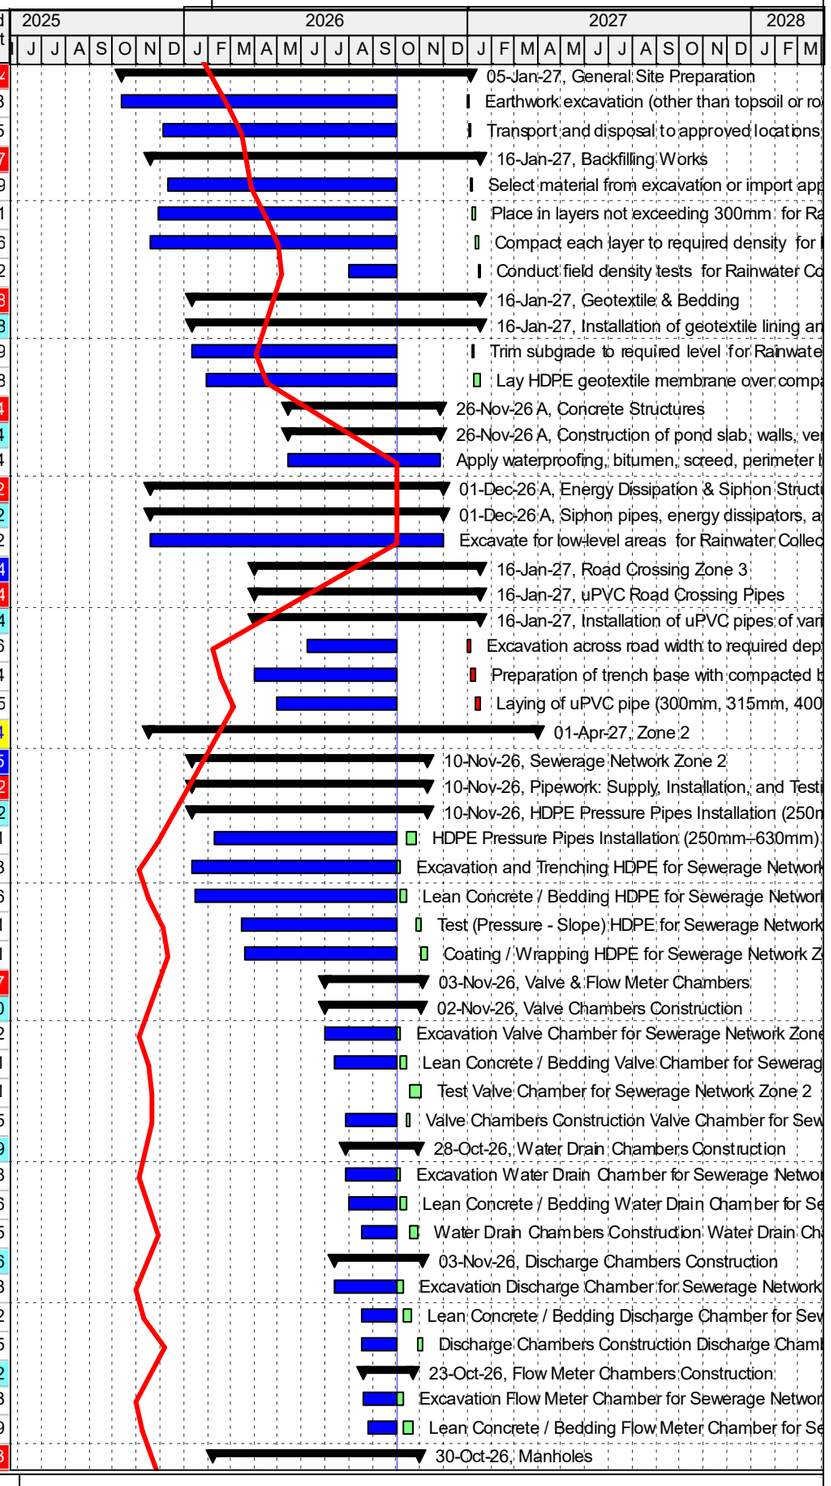


Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary

TASK filter: 2 Weeks Ahead.

© Oracle Corporation

Development of Phase One – Part Two – Third Industrial


Activity ID	Activity Name	Original Duration	BL Project Start	BL Project Finish	Start	Finish	Budgeted Total Cost
1200mm GRP Manholes with Backdrop		224	09-Nov-25	04-Jan-26	07-Feb-26 A	24-Oct-26	$549,417.87
MOD-SWN-	1200mm GRP Manholes with Backdrop 1.2m GRP for Sewerage Network Zone 2	21	30-Nov-25	20-Dec-25	14-Feb-26 A	09-Oct-26	$380,366.22
MOD-SWN-	Lean Concrete / Bedding 1.2m GRP for Sewerage Network Zone 2	21	09-Nov-25	29-Nov-25	07-Feb-26 A	06-Oct-26	$84,525.83
MOD-SWN-	Test 1.2m GRP for Sewerage Network Zone 2	15	21-Dec-25	04-Jan-26	09-Oct-26	24-Oct-26	$84,525.83
1500mm GRP Manholes (Standard & Backdrop)		227	09-Nov-25	25-Jan-26	14-Feb-26 A	27-Oct-26	$520,344.32
MOD-SWN-	1500mm GRP Manholes (Standard & Backdrop) 1.5m GRP for Sewerage Network Zone	21	21-Dec-25	10-Jan-26	25-Feb-26 A	12-Oct-26	$360,238.37
MOD-SWN-	Lean Concrete / Bedding 1.5m GRP for Sewerage Network Zone 2	21	09-Nov-25	29-Nov-25	14-Feb-26 A	07-Oct-26	$80,052.97
MOD-SWN-	Test 1.5m GRP for Sewerage Network Zone 2	15	11-Jan-26	25-Jan-26	12-Oct-26	27-Oct-26	$80,052.97
1800mm GRP Manholes (Standard & Backdrop)		229	09-Nov-25	11-Feb-26	16-Feb-26 A	29-Oct-26	$25,958.62
MOD-SWN-	1800mm GRP Manholes (Standard & Backdrop) 1.8m GRP for Sewerage Network Zone	17	11-Jan-26	27-Jan-26	28-Feb-26 A	14-Oct-26	$17,971.35
MOD-SWN-	Lean Concrete / Bedding 1.8m GRP for Sewerage Network Zone 2	21	09-Nov-25	29-Nov-25	16-Feb-26 A	06-Oct-26	$3,993.63
MOD-SWN-	Test 1.8m GRP for Sewerage Network Zone 2	15	28-Jan-26	11-Feb-26	14-Oct-26	29-Oct-26	$3,993.63
2000mm GRP Manholes (Standard & Backdrop)		230	09-Nov-25	17-Feb-26	16-Mar-26 A	30-Oct-26	$8,220.58
MOD-SWN-	2000mm GRP Manholes (Standard & Backdrop) 2m GRP for Sewerage Network Zone 2	6	28-Jan-26	02-Feb-26	22-Mar-26 A	15-Oct-26	$5,691.17
MOD-SWN-	Lean Concrete / Bedding 2m GRP for Sewerage Network Zone 2	21	09-Nov-25	29-Nov-25	16-Mar-26 A	06-Oct-26	$1,264.70
MOD-SWN-	Test 2m GRP for Sewerage Network Zone 2	15	03-Feb-26	17-Feb-26	15-Oct-26	30-Oct-26	$1,264.70
Rainwater Drainage Network Zone 2		252	27-Nov-25	18-Jan-26	01-Dec-25 A	24-Oct-26	4,091,562.4
Pipe Laying Works		21	14-Dec-25	05-Jan-26	04-Jan-26 A	07-Oct-26	$16,851.43
uPVC Connection Pipes (150mm dia)		21	14-Dec-25	05-Jan-26	04-Jan-26 A	07-Oct-26	$16,851.43
MOD-RWN-	Backfilling & compaction UPVC Con. for Rainwater Drainage Network Zone 2	2	04-Jan-26	05-Jan-26	04-Jan-26 A	07-Oct-26	$8,425.71
MOD-RWN-	Coating / Wrapping UPVC Con. for Rainwater Drainage Network Zone 2	21	14-Dec-25	03-Jan-26	12-Jan-26 A	07-Oct-26	$8,425.71
Precast Concrete Box Culverts		129	27-Nov-25	08-Jan-26	18-Apr-26 A	24-Oct-26	1,329,047.7
Box Culverts (500x500mm to 3500x800mm)		126	27-Nov-25	30-Dec-25	27-Apr-26 A	20-Oct-26	1,293,242.8
MOD-RWN-	Dewatering and trench shoring Box culvert for Rainwater Drainage Network Zone 2	7	27-Nov-25	06-Dec-25	27-Apr-26 A	06-Oct-26	$424,014.04
MOD-RWN-	Bedding preparation (gravel/lean concrete) Box culvert for Rainwater Drainage Network Z	6	06-Dec-25	13-Dec-25	30-Apr-26 A	10-Oct-26	$159,005.27
MOD-RWN-	Installation of box culvert units Box culvert for Rainwater Drainage Network Zone 2	5	13-Dec-25	25-Dec-25	10-Oct-26	15-Oct-26	$636,021.07
MOD-RWN-	Alignment and joint sealing Box culvert for Rainwater Drainage Network Zone 2	4	25-Dec-25	30-Dec-25	15-Oct-26	20-Oct-26	$74,202.46
Tube Culverts at Road Intersections		11	30-Nov-25	13-Dec-25	18-Apr-26 A	10-Oct-26	$25,056.68
MOD-RWN-	Trench excavation under road Tube culvert for Rainwater Drainage Network Zone 2	11	30-Nov-25	13-Dec-25	18-Apr-26 A	10-Oct-26	$25,056.68
Box Culverts at Road Intersections		17	20-Dec-25	08-Jan-26	05-Oct-26	24-Oct-26	$10,748.19
MOD-RWN-	Install precast box culvert for Rainwater Drainage Network Zone 2	4	20-Dec-25	24-Dec-25	05-Oct-26	08-Oct-26	$9,377.62
MOD-RWN-	Construct connection chambers (if needed) for Rainwater Drainage Network Zone 2	1	24-Dec-25	25-Dec-25	10-Oct-26	10-Oct-26	$1,082.03
MOD-RWN-	Joint treatment and testing for Rainwater Drainage Network Zone 2	12	25-Dec-25	08-Jan-26	11-Oct-26	24-Oct-26	$288.54
Manholes		173	13-Dec-25	15-Jan-26	05-Jan-26 A	21-Oct-26	1,360,040.8
Circular GRP Manholes (1200–1800mm dia)		171	17-Dec-25	15-Jan-26	05-Jan-26 A	19-Oct-26	$434,546.64
MOD-RWN-	Dewatering and safety barriers Circular Manhole for Rainwater Drainage Network Zone 2	7	17-Dec-25	25-Dec-25	05-Jan-26 A	11-Oct-26	$139,512.34
MOD-RWN-	Concrete base construction Circular Manhole for Rainwater Drainage Network Zone 2	5	25-Dec-25	31-Dec-25	06-Jan-26 A	12-Oct-26	$137,225.25
MOD-RWN-	Install GRP manhole shaft sections Circular Manhole for Rainwater Drainage Network Zo	8	31-Dec-25	10-Jan-26	07-Jan-26 A	14-Oct-26	$114,354.38
MOD-RWN-	Place slab and cover frame Circular Manhole for Rainwater Drainage Network Zone 2	3	10-Jan-26	13-Jan-26	06-Jul-26 A	17-Oct-26	$34,306.31
MOD-RWN-	Waterproofing Circular Manhole for Rainwater Drainage Network Zone 2	2	13-Jan-26	15-Jan-26	17-Oct-26	19-Oct-26	$9,148.35
Concrete Manholes for 1500x1500 Box Pipes		109	18-Dec-25	07-Jan-26	16-Feb-26 A	21-Oct-26	$673,558.16
MOD-RWN-	Base slab and wall shuttering Concrete Manhole 1.5x1.5 for Rainwater Drainage Networl	4	18-Dec-25	23-Dec-25	16-Feb-26 A	11-Oct-26	$216,247.62
MOD-RWN-	Wall reinforcement and casting Concrete Manhole 1.5x1.5 for Rainwater Drainage Netw	6	23-Dec-25	30-Dec-25	01-Mar-26 A	14-Oct-26	$212,702.58
MOD-RWN-	Roof slab with openings Concrete Manhole 1.5x1.5 for Rainwater Drainage Network Zon	3	30-Dec-25	03-Jan-26	05-Jul-26 A	17-Oct-26	$177,252.15
MOD-RWN-	Masonry/benching works inside Concrete Manhole 1.5x1.5 for Rainwater Drainage Netw	2	03-Jan-26	05-Jan-26	17-Oct-26	19-Oct-26	$53,175.64
MOD-RWN-	Install cover and frame Concrete Manhole 1.5x1.5 for Rainwater Drainage Network Zone	2	05-Jan-26	07-Jan-26	19-Oct-26	21-Oct-26	$14,180.17
Concrete Manholes for 1000x1000 Box Pipes		112	13-Dec-25	25-Dec-25	02-Mar-26 A	20-Oct-26	$251,936.10
MOD-RWN-	Base slab and wall shuttering Concrete Manhole 1x1 for Rainwater Drainage Network Zo	2	17-Dec-25	20-Dec-25	12-Oct-26	14-Oct-26	$120,063.30
MOD-RWN-	Wall reinforcement and casting Concrete Manhole 1x1 for Rainwater Drainage Network Z	5	20-Dec-25	25-Dec-25	14-Oct-26	20-Oct-26	$118,095.04
MOD-RWN-	Excavation Concrete Manhole 1x1 for Rainwater Drainage Network Zone 2	4	13-Dec-25	17-Dec-25	02-Mar-26 A	12-Oct-26	$13,777.76

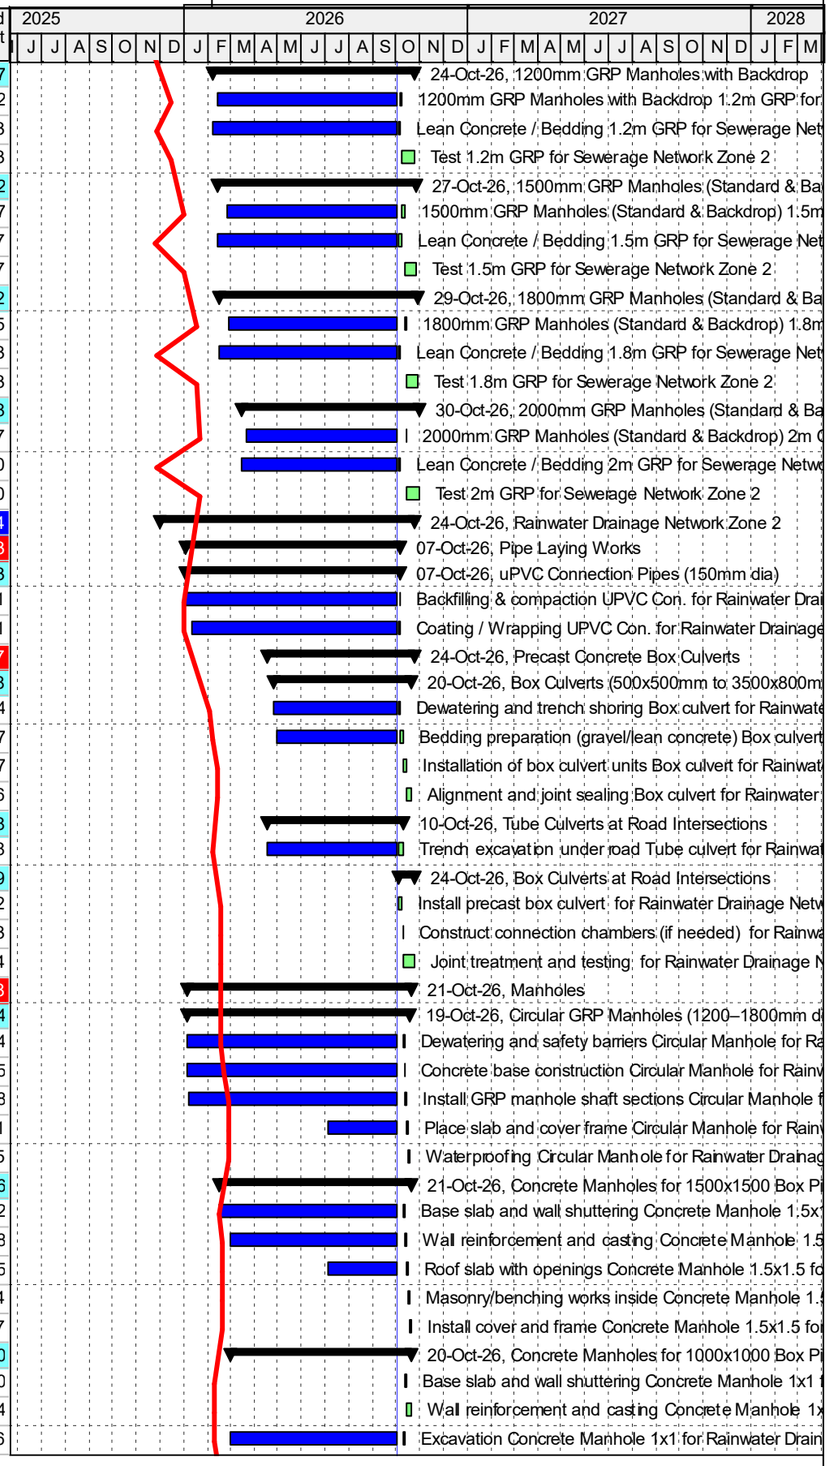

© Oracle Corporation

Development of Phase One – Part Two – Third Industrial

Activity ID	Activity Name	Original Duration	BL Project Start	BL Project Finish	Start	Finish	Budgeted Total Cost
Gully Outfalls to Swales		193	24-Dec-25	18-Jan-26	01-Feb-26 A	21-Oct-26	$314,878.93
Gully Outfalls to Swales		187	28-Dec-25	18-Jan-26	07-Feb-26 A	14-Oct-26	$254,733.51
MOD-RWN-	Excavate outfall channel Gully Outfall to Swales for Rainwater Drainage Network Zone 2	5	28-Dec-25	03-Jan-26	07-Feb-26 A	10-Oct-26	$56,607.45
MOD-RWN-	Place concrete apron or pipes Gully Outfall to Swales for Rainwater Drainage Network Zc	7	03-Jan-26	11-Jan-26	15-Feb-26 A	11-Oct-26	$127,366.76
MOD-RWN-	Provide slope protection (riprap) Gully Outfall to Swales for Rainwater Drainage Network Z	4	11-Jan-26	15-Jan-26	20-Feb-26 A	11-Oct-26	$42,455.59
MOD-RWN-	Compact and shape terrain Gully Outfall to Swales for Rainwater Drainage Network Zone	2	17-Jan-26	18-Jan-26	12-Oct-26	14-Oct-26	$28,303.72
Riprap Works & Protection		125	24-Dec-25	11-Jan-26	01-Feb-26 A	21-Oct-26	$60,145.41
MOD-RWN-	Lay filter fabric/membrane for Rainwater Drainage Network Zone 2	3	24-Dec-25	28-Dec-25	01-Feb-26 A	11-Oct-26	$7,075.93
MOD-RWN-	Place riprap/stone layer for Rainwater Drainage Network Zone 2	7	28-Dec-25	05-Jan-26	17-Feb-26 A	15-Oct-26	$38,917.62
MOD-RWN-	Compact edges for Rainwater Drainage Network Zone 2	5	05-Jan-26	11-Jan-26	15-Oct-26	21-Oct-26	$14,151.86
Backfilling & Bedding		31	09-Dec-25	06-Jan-26	01-Dec-25 A	12-Oct-26	1,070,743.5
Gravel Bedding & Filter Cloth for uPVC Drain Pipes		31	09-Dec-25	06-Jan-26	01-Dec-25 A	12-Oct-26	1,070,743.5
MOD-RWN-	Final fill and trench restoration for Rainwater Drainage Network Zone 2	8	28-Dec-25	06-Jan-26	01-Dec-25 A	12-Oct-26	$152,963.36
MOD-RWN-	Lay pipe within gravel zone for Rainwater Drainage Network Zone 2	9	09-Dec-25	20-Dec-25	03-Jan-26 A	07-Oct-26	$688,335.11
MOD-RWN-	Wrap filter cloth above pipe for Rainwater Drainage Network Zone 2	7	20-Dec-25	28-Dec-25	03-Jan-26 A	10-Oct-26	$229,445.04
Potable Water Network Zone 2		86	02-Dec-25	07-Jan-26	17-May-26 A	17-Oct-26	$410,912.93
Valve Installation & Chambers		10	21-Dec-25	31-Dec-25	05-Oct-26	17-Oct-26	$94,891.03
MOD-PWN-VC	Fixing Covers, Gratings, Frames for Potable Water Network Zone 2	6	21-Dec-25	27-Dec-25	05-Oct-26	12-Oct-26	$63,260.68
MOD-PWN-VC	Tagging & Painting for Potable Water Network Zone 2	4	28-Dec-25	31-Dec-25	12-Oct-26	17-Oct-26	$31,630.34
Flow Meter Installation		7	02-Dec-25	09-Dec-25	01-Sep-26 A	10-Oct-26	$18,460.85
MOD-PWN-FM	RC or Precast Chamber Construction for Potable Water Network Zone 2	7	02-Dec-25	09-Dec-25	01-Sep-26 A	10-Oct-26	$18,460.85
Washout & Air Valve Chambers		83	15-Dec-25	07-Jan-26	17-May-26 A	12-Oct-26	$297,561.06
MOD-PWN-W/	Washout (Valve + Outlet) Installation for Potable Water Network Zone 2	10	15-Dec-25	25-Dec-25	17-May-26 A	07-Oct-26	$129,538.51
MOD-PWN-W/	Air Valve Rooms (Valve + Outlet) Installation for Potable Water Network Zone 2	5	27-Dec-25	31-Dec-25	11-Aug-26 A	08-Oct-26	$90,150.20
MOD-PWN-W/	Covers, Ladders & Tags for Potable Water Network Zone 2	4	01-Jan-26	05-Jan-26	17-Sep-26 A	10-Oct-26	$38,936.18
MOD-PWN-W/	Backfilling & Final Finishing for Potable Water Network Zone 2	2	06-Jan-26	07-Jan-26	10-Oct-26	12-Oct-26	$38,936.18
Irrigation Network Zone 2		36	25-Dec-25	10-Jan-26	01-Jul-26 A	31-Oct-26	$52,469.17
Valves and Appurtenances		4	25-Dec-25	29-Dec-25	04-Jul-26 A	07-Oct-26	$7,631.86
MOD-IRN-VA-3	Valve Pressure Testing for Irrigation Network Zone 2	2	25-Dec-25	27-Dec-25	04-Jul-26 A	06-Oct-26	$3,179.94
MOD-IRN-VA-4	Support Brackets/Anchor Blocks for Irrigation Network Zone 2	2	28-Dec-25	29-Dec-25	07-Jul-26 A	07-Oct-26	$4,451.92
Flow Meter Chambers		6	03-Jan-26	10-Jan-26	01-Jul-26 A	31-Oct-26	$44,837.31
MOD-IRN-FC-2	Flow Meter Installation (280, 300, 500 mm) Flow Meter Chamber for Irrigation Network Z	5	03-Jan-26	07-Jan-26	01-Jul-26 A	31-Oct-26	$31,386.12
MOD-IRN-FC-3	Integration with Pipework Flow Meter Chamber for Irrigation Network Zone 2	2	08-Jan-26	10-Jan-26	02-Jul-26 A	31-Oct-26	$13,451.19
Rainwater Collection Ponds Zone 2		154	22-Jan-26	27-Sep-26	17-Nov-25 A	01-Apr-27	$632,912.32
Excavation for Rainwater Drainage Pond		23	22-Jan-26	05-Mar-26	08-Jun-26 A	04-Jan-27	$104,861.93
Deep excavation, backfill, disposal for pond formation		23	22-Jan-26	05-Mar-26	08-Jun-26 A	04-Jan-27	$104,861.93
MOD-RCP-E	Excavate in layers to final depth for Rainwater Collection Ponds Zone 2	12	22-Jan-26	04-Feb-26	08-Jun-26 A	02-Jan-27	$34,390.20
MOD-RCP-E	Dewater during excavation for Rainwater Collection Ponds Zone 2	5	05-Feb-26	10-Feb-26	07-Jul-26 A	03-Jan-27	$33,826.43
MOD-RCP-E	Place warning tapes for Rainwater Collection Ponds Zone 2	6	11-Feb-26	19-Feb-26	21-Jul-26 A	03-Jan-27	$8,456.61
MOD-RCP-E	Dispose of rock/materials to approved dump area for Rainwater Collection Ponds Zone :	7	19-Feb-26	05-Mar-26	01-Aug-26 A	04-Jan-27	$28,188.69
Backfilling Works		142	08-Jun-26	17-Aug-26	17-Nov-25 A	16-Jan-27	$229,230.51
MOD-RCP-BW	Place in layers not exceeding 300mm for Rainwater Collection Ponds Zone 2	21	25-Jun-26	20-Jul-26	17-Nov-25 A	10-Jan-27	$84,453.34
MOD-RCP-BW	Compact each layer to required density for Rainwater Collection Ponds Zone 2	20	20-Jul-26	12-Aug-26	25-Nov-25 A	14-Jan-27	$60,323.82
MOD-RCP-BW	Conduct field density tests for Rainwater Collection Ponds Zone 2	4	12-Aug-26	17-Aug-26	01-Aug-26 A	16-Jan-27	$36,194.29
MOD-RCP-BW	Select material from excavation or import approved material for Rainwater Collection Po	15	08-Jun-26	25-Jun-26	18-Nov-25 A	05-Jan-27	$48,259.05
Geotextile & Bedding		42	04-Jul-26	22-Aug-26	17-Jan-26 A	17-Feb-27	$266,117.42
Installation of geotextile lining and coarse sand bedding		42	04-Jul-26	22-Aug-26	17-Jan-26 A	17-Feb-27	$266,117.42
MOD-RCP-C	Lay HDPE geotextile membrane over compacted soil for Rainwater Collection Ponds Zo	21	04-Jul-26	28-Jul-26	17-Jan-26 A	19-Jan-27	$143,293.99
MOD-RCP-C	Place 500mm thick coarse sand bedding for Rainwater Collection Ponds Zone 2	21	28-Jul-26	22-Aug-26	22-Jul-26 A	17-Feb-27	$122,823.42
Concrete Structures		8	16-Sep-26	27-Sep-26	20-Sep-26 A	01-Apr-27	$32,702.46
Construction of pond slab, walls, vertical structures		8	16-Sep-26	27-Sep-26	20-Sep-26 A	01-Apr-27	$32,702.46

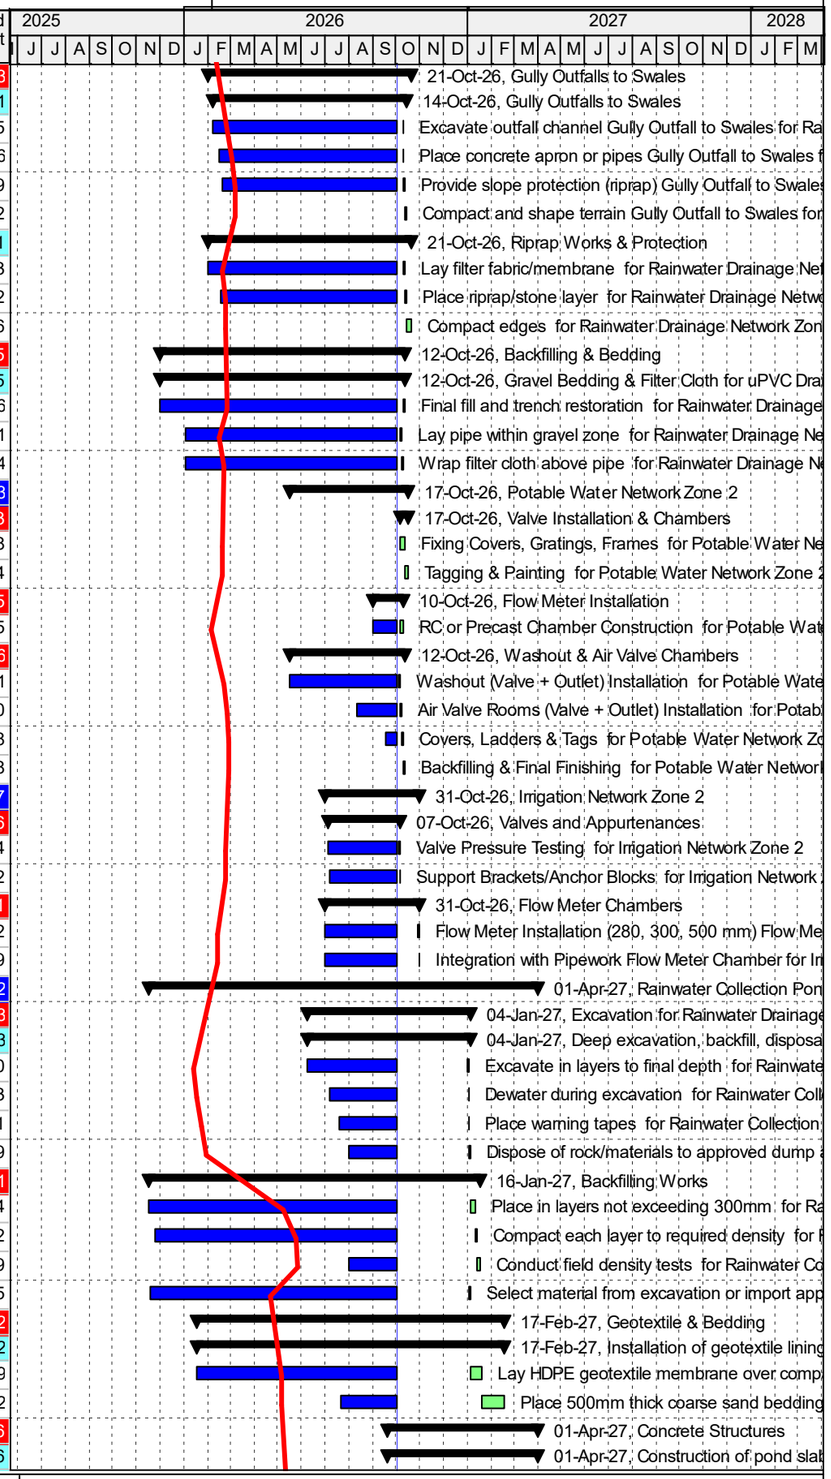


Actual Level of Effort · Actual Work · Remaining Work · Critical Remaining Work · Milestone · summary

TASK filter: 2 Weeks Ahead.

© Oracle Corporation

Development of Phase One – Part Two – Third Industrial

Activity ID	Activity Name	Original Duration	BL Project Start	BL Project Finish	Start	Finish	Budgeted Total Cost
MOD-RCP-(	Install formwork and reinforcement for Rainwater Collection Ponds Zone 2	8	16-Sep-26	27-Sep-26	20-Sep-26 A	01-Apr-27	$32,702.46
Zone 1		340	19-Oct-25	11-Oct-26	03-Sep-25 A	04-Feb-27	15,474,393.7
Sewerage Network Zone 1		287	19-Oct-25	03-Feb-26	11-Dec-25 A	17-Nov-26	1,382,533.6
Pipework: Supply, Installation, and Testing		58	05-Jan-26	03-Feb-26	11-Dec-25 A	10-Oct-26	$41,673.43
HDPE Pressure Pipes Installation (250mm–630mm)		58	05-Jan-26	03-Feb-26	11-Dec-25 A	10-Oct-26	$41,673.43
MOD-SWN-	Backfilling & Warming Tape HDPE for Sewerage Network Zone 1	15	20-Jan-26	03-Feb-26	05-Feb-26 A	10-Oct-26	$20,836.71
MOD-SWN-	Coating / Wrapping HDPE for Sewerage Network Zone 1	15	05-Jan-26	19-Jan-26	11-Dec-25 A	06-Oct-26	$20,836.71
Fittings and Valves		14	21-Dec-25	05-Jan-26	05-Oct-26	21-Oct-26	$32,098.68
MOD-SWN-FV-	Supply & Installation of HDPE Elbows for Sewerage Network Zone 1	6	21-Dec-25	27-Dec-25	05-Oct-26	12-Oct-26	$13,652.43
MOD-SWN-FV-	Gate Valves Installation for Sewerage Network Zone 1	4	28-Dec-25	31-Dec-25	12-Oct-26	17-Oct-26	$9,660.60
MOD-SWN-FV-	Drain Valves Installation for Sewerage Network Zone 1	4	01-Jan-26	05-Jan-26	17-Oct-26	21-Oct-26	$8,785.65
Valve & Flow Meter Chambers		134	19-Oct-25	11-Jan-26	01-Jun-26 A	17-Nov-26	$74,373.00
Valve Chambers Construction		48	19-Oct-25	05-Dec-25	01-Jun-26 A	30-Oct-26	$9,651.69
MOD-SWN-	Excavation Valve Chamber for Sewerage Network Zone 1	21	19-Oct-25	08-Nov-25	01-Jun-26 A	13-Oct-26	$2,068.22
MOD-SWN-	Lean Concrete / Bedding Valve Chamber for Sewerage Network Zone 1	21	09-Nov-25	29-Nov-25	09-Jun-26 A	26-Oct-26	$1,378.81
MOD-SWN-	Valve Chambers Construction Valve Chamber for Sewerage Network Zone 1	6	30-Nov-25	05-Dec-25	23-Jun-26 A	30-Oct-26	$6,204.65
Water Drain Chambers Construction		130	19-Oct-25	08-Jan-26	11-Jul-26 A	12-Nov-26	$35,830.84
MOD-SWN-	Excavation Water Drain Chamber for Sewerage Network Zone 1	21	19-Oct-25	08-Nov-25	11-Jul-26 A	09-Oct-26	$6,718.28
MOD-SWN-	Lean Concrete / Bedding Water Drain Chamber for Sewerage Network Zone 1	21	09-Nov-25	29-Nov-25	22-Jul-26 A	17-Oct-26	$4,478.86
MOD-SWN-	Test Water Drain Chamber for Sewerage Network Zone 1	15	25-Dec-25	08-Jan-26	01-Aug-26 A	12-Nov-26	$4,478.86
MOD-SWN-	Water Drain Chambers Construction Water Drain Chamber for Sewerage Network Zone	19	06-Dec-25	24-Dec-25	29-Jul-26 A	06-Nov-26	$20,154.85
Discharge Chambers Construction		71	19-Oct-25	06-Jan-26	13-Jul-26 A	15-Nov-26	$21,901.06
MOD-SWN-	Excavation Discharge Chamber for Sewerage Network Zone 1	21	19-Oct-25	08-Nov-25	13-Jul-26 A	13-Oct-26	$4,693.08
MOD-SWN-	Lean Concrete / Bedding Discharge Chamber for Sewerage Network Zone 1	21	09-Nov-25	29-Nov-25	14-Jul-26 A	26-Oct-26	$3,128.72
MOD-SWN-	Discharge Chambers Construction Discharge Chamber for Sewerage Network Zone 1	13	25-Dec-25	06-Jan-26	29-Jul-26 A	15-Nov-26	$14,079.25
Flow Meter Chambers Construction		39	19-Oct-25	11-Jan-26	11-Jul-26 A	17-Nov-26	$6,989.41
MOD-SWN-	Excavation Flow Meter Chamber for Sewerage Network Zone 1	21	19-Oct-25	08-Nov-25	11-Jul-26 A	10-Oct-26	$1,497.73
MOD-SWN-	Lean Concrete / Bedding Flow Meter Chamber for Sewerage Network Zone 1	21	09-Nov-25	29-Nov-25	28-Jul-26 A	19-Oct-26	$998.49
MOD-SWN-	Flow Meter Chambers Construction Flow Meter Chamber for Sewerage Network Zone 1	5	07-Jan-26	11-Jan-26	01-Aug-26 A	17-Nov-26	$4,493.20
Manholes		20	05-Dec-25	08-Jan-26	04-Oct-26	24-Oct-26	$509,511.41
1200mm GRP Manholes with Backdrop		20	05-Dec-25	24-Dec-25	04-Oct-26	24-Oct-26	$253,577.48
MOD-SWN-	Backfilling 1.2m GRP for Sewerage Network Zone 1	15	10-Dec-25	24-Dec-25	09-Oct-26	24-Oct-26	$169,051.65
MOD-SWN-	Test 1.2m GRP for Sewerage Network Zone 1	5	05-Dec-25	09-Dec-25	04-Oct-26	09-Oct-26	$84,525.83
1500mm GRP Manholes (Standard & Backdrop)		20	10-Dec-25	29-Dec-25	04-Oct-26	24-Oct-26	$240,158.92
MOD-SWN-	Backfilling 1.5m GRP for Sewerage Network Zone 1	15	15-Dec-25	29-Dec-25	09-Oct-26	24-Oct-26	$160,105.94
MOD-SWN-	Test 1.5m GRP for Sewerage Network Zone 1	5	10-Dec-25	14-Dec-25	04-Oct-26	09-Oct-26	$80,052.97
1800mm GRP Manholes (Standard & Backdrop)		20	11-Dec-25	30-Dec-25	04-Oct-26	24-Oct-26	$11,980.90
MOD-SWN-	Backfilling 1.8m GRP for Sewerage Network Zone 1	15	16-Dec-25	30-Dec-25	09-Oct-26	24-Oct-26	$7,987.27
MOD-SWN-	Test 1.8m GRP for Sewerage Network Zone 1	5	11-Dec-25	15-Dec-25	04-Oct-26	09-Oct-26	$3,993.63
2000mm GRP Manholes (Standard & Backdrop)		20	20-Dec-25	08-Jan-26	04-Oct-26	24-Oct-26	$3,794.11
MOD-SWN-	Backfilling 2m GRP for Sewerage Network Zone 1	15	25-Dec-25	08-Jan-26	09-Oct-26	24-Oct-26	$2,529.41
MOD-SWN-	Test 2m GRP for Sewerage Network Zone 1	5	20-Dec-25	24-Dec-25	04-Oct-26	09-Oct-26	$1,264.70
Pumping Stations		145	19-Nov-25	27-Dec-25	01-Jan-26 A	03-Nov-26	$724,877.10
Perimeter Walls & Gates		10	01-Dec-25	11-Dec-25	30-Jul-26 A	07-Oct-26	$27,650.44
MOD-SWN-	Main entrance gates – Each PS for Sewerage Network Zone 1	10	01-Dec-25	11-Dec-25	30-Jul-26 A	07-Oct-26	$27,650.44
Engine/Motor Control Center Buildings		7	01-Dec-25	08-Dec-25	04-Oct-26	11-Oct-26	$42,052.73
MOD-SWN-	MCC Building – PS2 for Sewerage Network Zone 1	7	01-Dec-25	08-Dec-25	04-Oct-26	11-Oct-26	$42,052.73
Pump Well and Valve Chambers		27	19-Nov-25	20-Dec-25	04-Oct-26	03-Nov-26	$197,138.61
MOD-SWN-	Pump well & valve chamber structure – PS1 (2 wells, 12m deep) for Sewerage Network	13	19-Nov-25	03-Dec-25	04-Oct-26	18-Oct-26	$74,197.09
MOD-SWN-	Concrete wall (5x5x1m) inside PS1 well for Sewerage Network Zone 1	7	04-Dec-25	11-Dec-25	19-Oct-26	26-Oct-26	$41,284.68

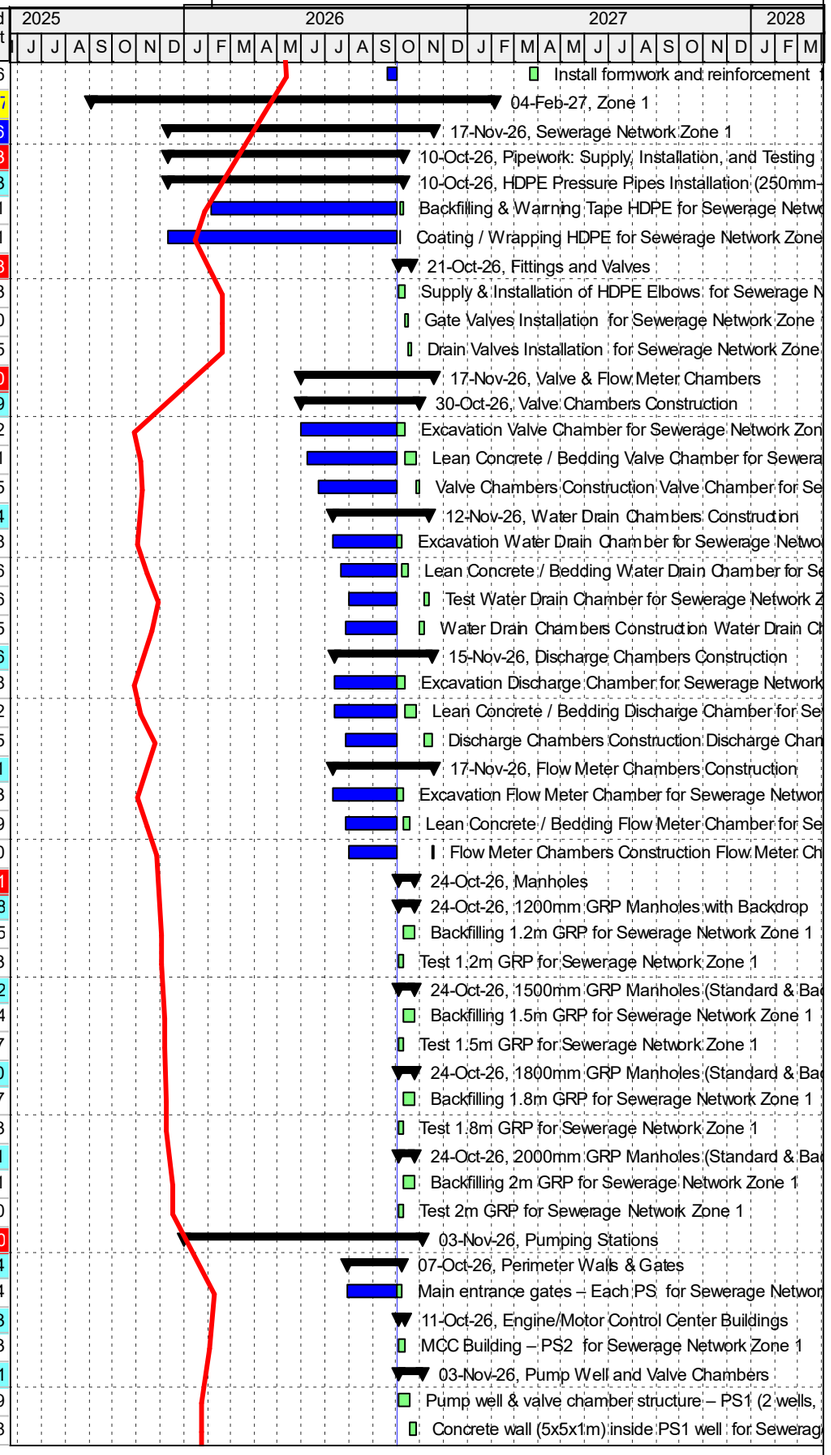


Actual Level of Effort · Actual Work · Remaining Work · Critical Remaining Work · Milestone · summary

TASK filter: 2 Weeks Ahead.

© Oracle Corporation

Development of Phase One – Part Two – Third Industrial

Activity ID	Activity Name	Original Duration	BL Project Start	BL Project Finish	Start	Finish	Budgeted Total Cost
MOD-SWN-	Pump well & valve chamber structure – PS2 (2 wells, 3m each, 9m depth) for Sewerage	14	04-Dec-25	20-Dec-25	19-Oct-26	03-Nov-26	$81,656.84
Lighting Works		13	13-Dec-25	27-Dec-25	01-Jan-26 A	29-Oct-26	$384,043.12
MOD-SWN-	250W Flood Light installation – Each PS for Sewerage Network Zone 1	13	13-Dec-25	27-Dec-25	01-Jan-26 A	29-Oct-26	$384,043.12
Duct Works		1	04-Dec-25	04-Dec-25	19-Oct-26	19-Oct-26	$2,760.41
MOD-SWN-	uPVC duct Track 1 – All PSs for Sewerage Network Zone 1	1	04-Dec-25	04-Dec-25	19-Oct-26	19-Oct-26	$2,760.41
Landscaping / Interlocking Tiles		17	06-Dec-25	24-Dec-25	05-Oct-26	24-Oct-26	$50,952.81
MOD-SWN-	Building perimeter interlock tiles for Sewerage Network Zone 1	17	06-Dec-25	24-Dec-25	05-Oct-26	24-Oct-26	$50,952.81
Pumping Station Internal Drainage Network		7	01-Dec-25	08-Dec-25	03-Oct-26	10-Oct-26	$20,278.98
MOD-SWN-	Internal surface drainage channels for Sewerage Network Zone 1	7	01-Dec-25	08-Dec-25	03-Oct-26	10-Oct-26	$20,278.98
Rainwater Drainage Network Zone 1		294	24-Nov-25	18-Jan-26	01-Jan-26 A	25-Oct-26	3,416,198.4
Pipe Laying Works		49	06-Dec-25	05-Jan-26	08-Jan-26 A	11-Oct-26	$100,666.07
Supply & Installation of uPVC Pipes (250–300mm dia)		8	06-Dec-25	13-Dec-25	10-Jan-26 A	06-Oct-26	$75,388.93
MOD-RWN-	Backfilling & Warning Tape UPVC for Rainwater Drainage Network Zone 1	8	06-Dec-25	13-Dec-25	10-Jan-26 A	06-Oct-26	$75,388.93
uPVC Connection Pipes (150mm dia)		23	11-Dec-25	05-Jan-26	08-Jan-26 A	11-Oct-26	$25,277.14
MOD-RWN-	Test (Pressure-slope) UPVC Con. for Rainwater Drainage Network Zone 1	3	11-Dec-25	13-Dec-25	08-Jan-26 A	06-Oct-26	$8,425.71
MOD-RWN-	Backfilling & compaction UPVC Con. for Rainwater Drainage Network Zone 1	2	04-Jan-26	05-Jan-26	11-Jan-26 A	11-Oct-26	$8,425.71
MOD-RWN-	Coating / Wrapping UPVC Con. for Rainwater Drainage Network Zone 1	21	14-Dec-25	03-Jan-26	10-Jan-26 A	10-Oct-26	$8,425.71
Precast Concrete Box Culverts		121	24-Nov-25	04-Jan-26	28-Apr-26 A	24-Oct-26	1,050,622.8
Box Culverts (500x500mm to 3500x800mm)		121	25-Nov-25	03-Jan-26	28-Apr-26 A	24-Oct-26	$890,429.49
MOD-RWN-	Installation of box culvert units Box culvert for Rainwater Drainage Network Zone 1	8	25-Nov-25	11-Dec-25	28-Apr-26 A	10-Oct-26	$636,021.07
MOD-RWN-	Alignment and joint sealing Box culvert for Rainwater Drainage Network Zone 1	4	13-Dec-25	16-Dec-25	05-May-26 A	12-Oct-26	$74,202.46
MOD-RWN-	Construct headwalls/wing walls (if needed) Box culvert for Rainwater Drainage Network Z	5	17-Dec-25	25-Dec-25	12-Oct-26	18-Oct-26	$106,003.51
MOD-RWN-	Backfilling and compaction Box culvert for Rainwater Drainage Network Zone 1	5	27-Dec-25	03-Jan-26	18-Oct-26	24-Oct-26	$74,202.46
Tube Culverts at Road Intersections		114	24-Nov-25	04-Jan-26	12-May-26 A	21-Oct-26	$149,445.20
MOD-RWN-	Pipe bedding and twin pipe alignment Tube culvert for Rainwater Drainage Network Zone	6	24-Nov-25	01-Dec-25	12-May-26 A	06-Oct-26	$13,423.22
MOD-RWN-	Pipe laying and jointing Tube culvert for Rainwater Drainage Network Zone 1	10	01-Dec-25	25-Dec-25	24-May-26 A	12-Oct-26	$118,124.35
MOD-RWN-	Backfilling and road reinstatement Tube culvert for Rainwater Drainage Network Zone 1	8	25-Dec-25	04-Jan-26	12-Oct-26	21-Oct-26	$17,897.63
Box Culverts at Road Intersections		15	02-Dec-25	22-Dec-25	04-Oct-26	21-Oct-26	$10,748.19
MOD-RWN-	Install precast box culvert for Rainwater Drainage Network Zone 1	4	02-Dec-25	07-Dec-25	04-Oct-26	08-Oct-26	$9,377.62
MOD-RWN-	Construct connection chambers (if needed) for Rainwater Drainage Network Zone 1	1	07-Dec-25	08-Dec-25	08-Oct-26	10-Oct-26	$1,082.03
MOD-RWN-	Joint treatment and testing for Rainwater Drainage Network Zone 1	10	08-Dec-25	22-Dec-25	10-Oct-26	21-Oct-26	$288.54
Manholes		143	25-Nov-25	18-Jan-26	01-Jan-26 A	25-Oct-26	1,494,838.4
Circular GRP Manholes (1200–1800mm dia)		43	01-Dec-25	18-Jan-26	01-Jan-26 A	24-Oct-26	$441,407.90
MOD-RWN-	Dewatering and safety barriers Circular Manhole for Rainwater Drainage Network Zone 1	10	01-Dec-25	11-Dec-25	01-Jan-26 A	08-Oct-26	$139,512.34
MOD-RWN-	Concrete base construction Circular Manhole for Rainwater Drainage Network Zone 1	5	13-Dec-25	17-Dec-25	03-Jan-26 A	10-Oct-26	$137,225.25
MOD-RWN-	Install GRP manhole shaft sections Circular Manhole for Rainwater Drainage Network Zo	13	18-Dec-25	01-Jan-26	06-Jan-26 A	15-Oct-26	$114,354.38
MOD-RWN-	Place slab and cover frame Circular Manhole for Rainwater Drainage Network Zone 1	6	03-Jan-26	08-Jan-26	11-Jan-26 A	18-Oct-26	$34,306.31
MOD-RWN-	Waterproofing Circular Manhole for Rainwater Drainage Network Zone 1	5	10-Jan-26	14-Jan-26	12-Jan-26 A	21-Oct-26	$9,148.35
MOD-RWN-	Backfilling and compaction Circular Manhole for Rainwater Drainage Network Zone 1	3	15-Jan-26	18-Jan-26	13-Jan-26 A	24-Oct-26	$6,861.26
Concrete Manholes for 1500x1500 Box Pipes		112	01-Dec-25	11-Jan-26	03-Jan-26 A	20-Oct-26	$673,558.16
MOD-RWN-	Base slab and wall shuttering Concrete Manhole 1.5x1.5 for Rainwater Drainage Networl	7	01-Dec-25	08-Dec-25	03-Jan-26 A	08-Oct-26	$216,247.62
MOD-RWN-	Wall reinforcement and casting Concrete Manhole 1.5x1.5 for Rainwater Drainage Netw	8	09-Dec-25	17-Dec-25	15-Feb-26 A	11-Oct-26	$212,702.58
MOD-RWN-	Roof slab with openings Concrete Manhole 1.5x1.5 for Rainwater Drainage Network Zon	5	18-Dec-25	23-Dec-25	17-Feb-26 A	12-Oct-26	$177,252.15
MOD-RWN-	Masonry/benching works inside Concrete Manhole 1.5x1.5 for Rainwater Drainage Netw	4	24-Dec-25	28-Dec-25	21-Feb-26 A	14-Oct-26	$53,175.64
MOD-RWN-	Install cover and frame Concrete Manhole 1.5x1.5 for Rainwater Drainage Network Zone	6	05-Jan-26	11-Jan-26	24-Feb-26 A	20-Oct-26	$14,180.17
Concrete Manholes for 1000x1000 Box Pipes		105	25-Nov-25	04-Jan-26	01-Jan-26 A	25-Oct-26	$379,872.39
MOD-RWN-	Excavation Concrete Manhole 1x1 for Rainwater Drainage Network Zone 1	6	25-Nov-25	01-Dec-25	01-Jan-26 A	08-Oct-26	$13,777.76
MOD-RWN-	Base slab and wall shuttering Concrete Manhole 1x1 for Rainwater Drainage Network Zo	4	02-Dec-25	06-Dec-25	01-Feb-26 A	10-Oct-26	$120,063.30
MOD-RWN-	Wall reinforcement and casting Concrete Manhole 1x1 for Rainwater Drainage Network Z	7	07-Dec-25	14-Dec-25	01-Apr-26 A	13-Oct-26	$118,095.04
MOD-RWN-	Roof slab with openings Concrete Manhole 1x1 for Rainwater Drainage Network Zone 1	8	15-Dec-25	23-Dec-25	06-Apr-26 A	18-Oct-26	$98,412.54

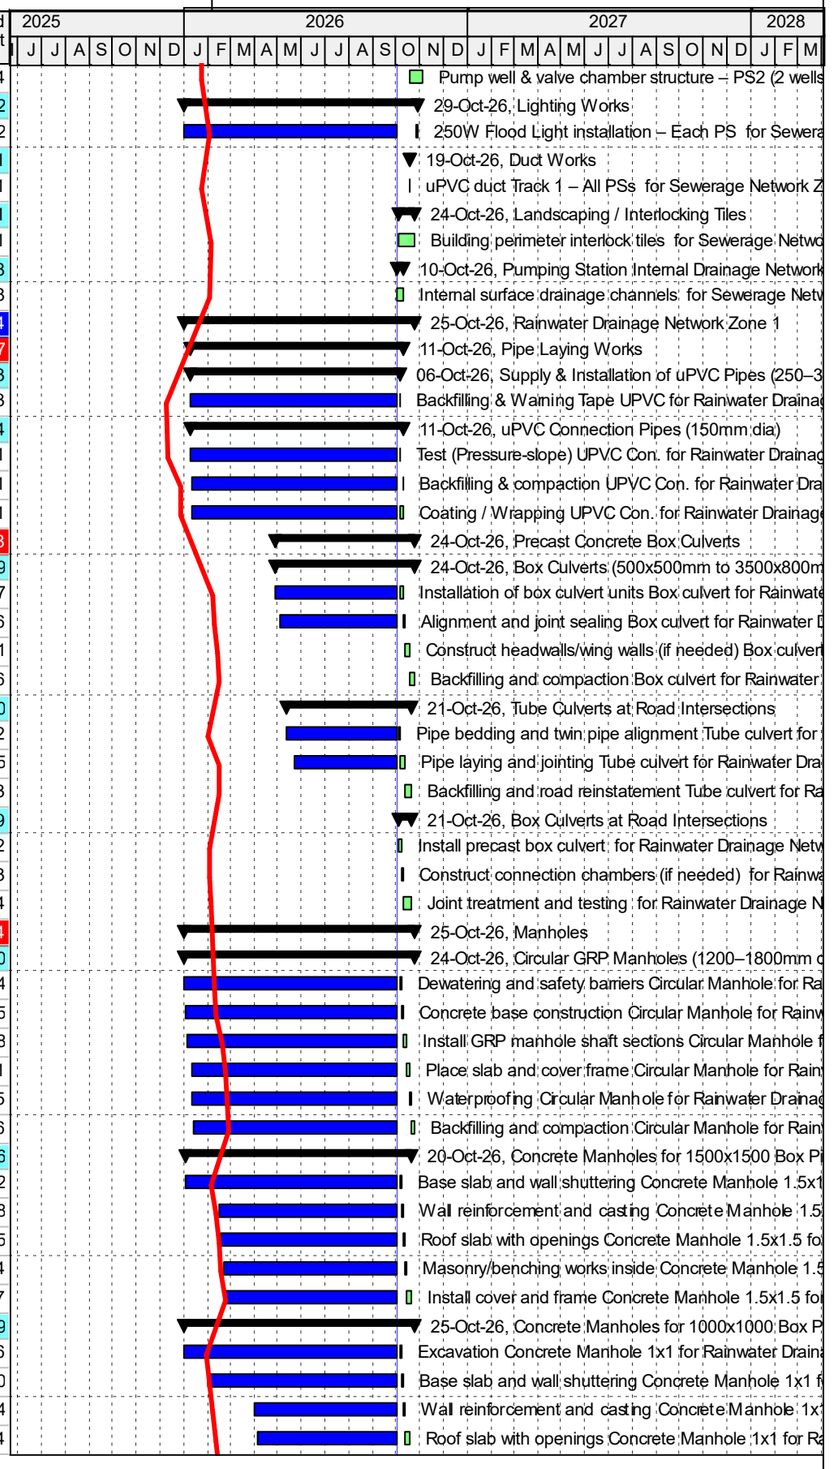


Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary

TASK filter: 2 Weeks Ahead.

© Oracle Corporation

Development of Phase One – Part Two – Third Industrial

Activity ID	Activity Name	Original Duration	BL Project Start	BL Project Finish	Start	Finish	Budgeted Total Cost
MOD-RWN-	Masonry/benching works inside Concrete Manhole 1x1 for Rainwater Drainage Network Z	10	24-Dec-25	04-Jan-26	21-Apr-26 A	25-Oct-26	$29,523.76
Chambers and Catch Basins		2	13-Jan-26	14-Jan-26	02-May-26 A	10-Oct-26	$52,160.51
Rainwater Catch Basins		2	13-Jan-26	14-Jan-26	02-May-26 A	10-Oct-26	$52,160.51
MOD-RWN-	Backfill and surface finish Catch Basin for Rainwater Drainage Network Zone 1	2	13-Jan-26	14-Jan-26	02-May-26 A	10-Oct-26	$52,160.51
Gully Outfalls to Swales		67	27-Dec-25	15-Jan-26	07-Jan-26 A	13-Oct-26	$258,271.48
Gully Outfalls to Swales		66	27-Dec-25	07-Jan-26	07-Jan-26 A	11-Oct-26	$198,126.07
MOD-RWN-	Place concrete apron or pipes Gully Outfall to Swales for Rainwater Drainage Network Zc	5	27-Dec-25	31-Dec-25	07-Jan-26 A	10-Oct-26	$127,366.76
MOD-RWN-	Provide slope protection (riprap) Gully Outfall to Swales for Rainwater Drainage Network Z	4	01-Jan-26	05-Jan-26	01-Feb-26 A	10-Oct-26	$42,455.59
MOD-RWN-	Compact and shape terrain Gully Outfall to Swales for Rainwater Drainage Network Zone	2	06-Jan-26	07-Jan-26	02-Apr-26 A	11-Oct-26	$28,303.72
Riprap Works & Protection		27	03-Jan-26	15-Jan-26	01-Feb-26 A	13-Oct-26	$60,145.41
MOD-RWN-	Lay filter fabric/membrane for Rainwater Drainage Network Zone 1	2	03-Jan-26	04-Jan-26	01-Feb-26 A	10-Oct-26	$7,075.93
MOD-RWN-	Place riprap/stone layer for Rainwater Drainage Network Zone 1	7	05-Jan-26	12-Jan-26	28-Feb-26 A	12-Oct-26	$38,917.62
MOD-RWN-	Compact edges for Rainwater Drainage Network Zone 1	3	13-Jan-26	15-Jan-26	01-Apr-26 A	13-Oct-26	$14,151.86
Backfilling & Bedding		12	05-Jan-26	18-Jan-26	05-Oct-26	19-Oct-26	$459,639.06
Backfilling Materials (Type A– 201–700mm Pipes)		6	12-Jan-26	18-Jan-26	06-Oct-26	13-Oct-26	$306,675.71
MOD-RWN-	Final fill to subgrade level for Rainwater Drainage Network Zone 1	6	12-Jan-26	18-Jan-26	06-Oct-26	13-Oct-26	$306,675.71
Gravel Bedding & Filter Cloth for uPVC Drain Pipes		12	05-Jan-26	18-Jan-26	05-Oct-26	19-Oct-26	$152,963.36
MOD-RWN-	Final fill and trench restoration for Rainwater Drainage Network Zone 1	12	05-Jan-26	18-Jan-26	05-Oct-26	19-Oct-26	$152,963.36
Potable Water Network Zone 1		100	25-Nov-25	06-Jan-26	07-May-26 A	13-Oct-26	$218,113.74
Valve Installation & Chambers		2	25-Dec-25	27-Dec-25	04-Oct-26	06-Oct-26	$31,630.34
MOD-PWN-VC	Tagging & Painting for Potable Water Network Zone 1	2	25-Dec-25	27-Dec-25	04-Oct-26	06-Oct-26	$31,630.34
Flow Meter Installation		8	25-Nov-25	03-Dec-25	07-May-26 A	07-Oct-26	$18,460.85
MOD-PWN-FM	RC or Precast Chamber Construction for Potable Water Network Zone 1	8	25-Nov-25	03-Dec-25	07-May-26 A	07-Oct-26	$18,460.85
Washout & Air Valve Chambers		24	22-Dec-25	06-Jan-26	16-Aug-26 A	13-Oct-26	$168,022.55
MOD-PWN-W/	Air Valve Rooms (Valve + Outlet) Installation for Potable Water Network Zone 1	7	22-Dec-25	29-Dec-25	16-Aug-26 A	07-Oct-26	$90,150.20
MOD-PWN-W/	Covers, Ladders & Tags for Potable Water Network Zone 1	4	30-Dec-25	03-Jan-26	14-Sep-26 A	10-Oct-26	$38,936.18
MOD-PWN-W/	Backfilling & Final Finishing for Potable Water Network Zone 1	3	04-Jan-26	06-Jan-26	10-Oct-26	13-Oct-26	$38,936.18
Irrigation Network Zone 1		68	28-Dec-25	18-Jan-26	01-Apr-26 A	05-Nov-26	$103,422.46
Valves and Appurtenances		2	28-Dec-25	29-Dec-25	01-Apr-26 A	06-Oct-26	$4,451.92
MOD-IRN-VA-0	Support Brackets/Anchor Blocks for Irrigation Network Zone 1	2	28-Dec-25	29-Dec-25	01-Apr-26 A	06-Oct-26	$4,451.92
Valve Rooms		16	10-Jan-26	18-Jan-26	05-Apr-26 A	07-Oct-26	$54,133.23
MOD-IRN-VR-0	Installation of Valve inside the Room Valve Chamber for Irrigation Network Zone 1	5	10-Jan-26	14-Jan-26	05-Apr-26 A	06-Oct-26	$30,074.02
MOD-IRN-VR-0	Fixing Frame & Cover Valve Chamber for Irrigation Network Zone 1	2	15-Jan-26	17-Jan-26	11-Jul-26 A	06-Oct-26	$18,044.41
MOD-IRN-VR-0	Backfilling and Finishing Valve Chamber for Irrigation Network Zone 1	1	18-Jan-26	18-Jan-26	13-Jul-26 A	07-Oct-26	$6,014.80
Flow Meter Chambers		6	06-Jan-26	14-Jan-26	01-Jul-26 A	05-Nov-26	$44,837.31
MOD-IRN-FC-0	Flow Meter Installation (280, 300, 500 mm) Flow Meter Chamber for Irrigation Network Z	6	06-Jan-26	12-Jan-26	01-Jul-26 A	05-Nov-26	$31,386.12
MOD-IRN-FC-0	Integration with Pipework Flow Meter Chamber for Irrigation Network Zone 1	2	13-Jan-26	14-Jan-26	02-Jul-26 A	05-Nov-26	$13,451.19
Rainwater Collection Ponds Zone 1		180	05-Feb-26	11-Oct-26	03-Sep-25 A	04-Feb-27	10,354,125.4
Excavation for Rainwater Drainage Pond		18	05-Feb-26	05-Mar-26	30-Nov-25 A	04-Jan-27	$105,707.59
Deep excavation, backfill, disposal for pond formation		18	05-Feb-26	05-Mar-26	30-Nov-25 A	04-Jan-27	$105,707.59
MOD-RCP-E	Dewater during excavation for Rainwater Collection Ponds Zone 1	5	05-Feb-26	10-Feb-26	30-Nov-25 A	02-Jan-27	$50,739.65
MOD-RCP-E	Place warning tapes for Rainwater Collection Ponds Zone 1	6	11-Feb-26	19-Feb-26	10-Dec-25 A	03-Jan-27	$12,684.91
MOD-RCP-E	Dispose of rock/materials to approved dump area for Rainwater Collection Ponds Zone	7	19-Feb-26	05-Mar-26	17-Dec-25 A	04-Jan-27	$42,283.04
General Site Preparation		42	02-Jul-26	20-Aug-26	08-Dec-25 A	16-Jan-27	9,443,984.2
MOD-RCP-GS-	Earthwork excavation (other than topsoil or rock) - Zone 1 (2 Ponds) - P3	21	02-Jul-26	27-Jul-26	10-Dec-25 A	09-Jan-27	5,126,449.2
MOD-RCP-GS-	Transport and disposal to approved locations - Zone 1 (2 Ponds) - P3	21	27-Jul-26	20-Aug-26	08-Dec-25 A	16-Jan-27	4,317,535.0
Backfilling Works		97	27-Jul-26	06-Oct-26	03-Sep-25 A	23-Jan-27	$343,845.76
MOD-RCP-BW	Select material from excavation or import approved material for Rainwater Collection Po	15	27-Jul-26	13-Aug-26	03-Sep-25 A	11-Jan-27	$72,388.58
MOD-RCP-BW	Place in layers not exceeding 300mm for Rainwater Collection Ponds Zone 1	21	13-Aug-26	07-Sep-26	03-Sep-25 A	16-Jan-27	$126,680.02
MOD-RCP-BW	Compact each layer to required density for Rainwater Collection Ponds Zone 1	20	07-Sep-26	01-Oct-26	16-Nov-25 A	20-Jan-27	$90,485.73
MOD-RCP-BW	Conduct field density tests for Rainwater Collection Ponds Zone 1	4	01-Oct-26	06-Oct-26	01-Aug-26 A	23-Jan-27	$54,291.44

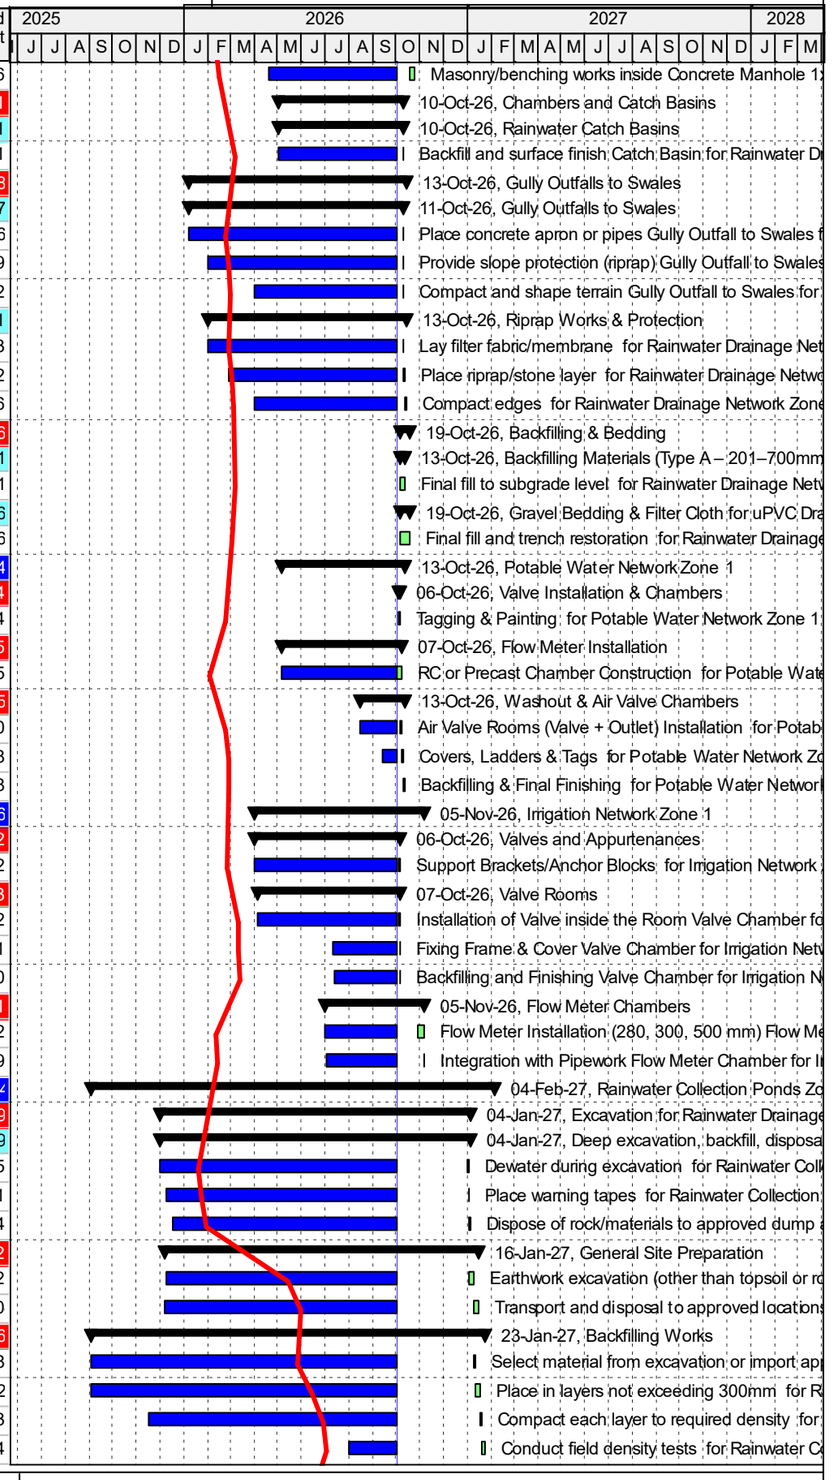


Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary

TASK filter: 2 Weeks Ahead.

© Oracle Corporation

Development of Phase One – Part Two – Third Industrial

Activity ID	Activity Name	Original Duration	BL Project Start	BL Project Finish	Start	Finish	Budgeted Total Cost
Geotextile & Bedding		49	13-Aug-26	11-Oct-26	07-Jan-26 A	04-Feb-27	$460,587.84
Installation of geotextile lining and coarse sand bedding		49	13-Aug-26	11-Oct-26	07-Jan-26 A	04-Feb-27	$460,587.84
MOD-RCP-(	Trim subgrade to required level for Rainwater Collection Ponds Zone 1	7	13-Aug-26	22-Aug-26	07-Jan-26 A	14-Jan-27	$61,411.71
MOD-RCP-(	Lay HDPE geotextile membrane over compacted soil for Rainwater Collection Ponds Zo	21	22-Aug-26	15-Sep-26	15-Jan-26 A	25-Jan-27	$214,940.99
MOD-RCP-(	Place 500mm thick coarse sand bedding for Rainwater Collection Ponds Zone 1	21	15-Sep-26	11-Oct-26	22-Jan-26 A	04-Feb-27	$184,235.14
General		219	10-May-26	25-Apr-27	04-Nov-25 A	18-Apr-27	8,257,220.5
Arterial Roads		37	10-May-26	01-Aug-26	27-Jun-26 A	08-Mar-27	$324,466.66
Precast Curbs (Type K1-D)		37	10-May-26	01-Aug-26	27-Jun-26 A	08-Mar-27	$324,466.66
MOD-ARR-PC-(	Excavation & Subgrade Prep for Arterial Roads	8	10-May-26	19-May-26	27-Jun-26 A	25-Jan-27	$46,352.38
MOD-ARR-PC-(	Concrete Base & Hunching for Arterial Roads	8	19-May-26	02-Jun-26	29-Jun-26 A	02-Feb-27	$46,352.38
MOD-ARR-PC-(	Curb Installation for Arterial Roads	21	07-Jul-26	01-Aug-26	01-Jul-26 A	08-Mar-27	$231,761.90
Communications		219	22-Jun-26	25-Apr-27	04-Nov-25 A	18-Apr-27	7,932,753.8
Ductworks		167	22-Jun-26	14-Feb-27	04-Nov-25 A	18-Apr-27	6,135,306.2
Concrete-Protected Service Culverts (50mm, 8 Outlets)		53	22-Jun-26	23-Aug-26	04-Nov-25 A	04-Mar-27	5,247,104.1
MOD-COC-[	Trench Excavation for Communications	10	22-Jun-26	08-Jul-26	04-Nov-25 A	24-Feb-27	1,749,034.7
MOD-COC-[	Culvert Installation & Concrete Protection for Communications	18	08-Jul-26	29-Jul-26	08-Nov-25 A	28-Feb-27	2,915,057.8
MOD-COC-[	Backfilling & Compaction for Communications	21	29-Jul-26	23-Aug-26	10-Nov-25 A	04-Mar-27	$583,011.57
Road Crossing Ducts (Exit 8)		121	16-Sep-26	14-Feb-27	01-Dec-25 A	18-Apr-27	$888,202.07
MOD-COC-[	Horizontal Directional Drilling (HDD) for Communications	21	16-Sep-26	12-Oct-26	01-Dec-25 A	07-Apr-27	$355,280.83
MOD-COC-[	Duct Installation & Joint Sealing for Communications	15	06-Jan-27	24-Jan-27	09-Dec-25 A	10-Apr-27	$355,280.83
MOD-COC-[	Asphalt/Paving Restoration for Communications	15	24-Jan-27	14-Feb-27	01-Apr-26 A	18-Apr-27	$177,640.41
Manholes (Telecom, 2000x1000x1001mm)		31	20-Mar-27	25-Apr-27	16-Dec-25 A	18-Apr-27	1,797,447.6
MOD-COC-MH-	Concrete Works - Foundation - Wall - Roof for Communications	10	20-Mar-27	31-Mar-27	16-Dec-25 A	18-Apr-27	1,198,298.4
MOD-COC-MH-	Frame/Cover Installation for Communications	21	31-Mar-27	25-Apr-27	17-Dec-25 A	18-Apr-27	$599,149.23
Testing & Commissioning & Closeout		157	12-Jan-26	18-May-27	14-Jan-26 A	08-May-27	17,343,453.8
Testing & Commissioning		157	12-Jan-26	18-May-27	14-Jan-26 A	08-May-27	17,343,453.8
Zone 3		77	12-Jan-26	09-Apr-26	20-Jan-26 A	20-Dec-26	2,891,237.2
A102060	Testing and Commissioning for Sewerage Network Zone 3	21	05-Mar-26	09-Apr-26	05-Mar-26 A	20-Dec-26	$350,278.50
A103590	Testing and Commissioning for Rain Water Drainage Network Zone 3	21	19-Jan-26	11-Feb-26	29-Jan-26 A	01-Dec-26	1,789,001.6
A103600	Testing and Commissioning for Potable Water Network Zone 3	21	19-Jan-26	11-Feb-26	31-Jan-26 A	28-Nov-26	$454,067.96
A103610	Testing and Commissioning for Irrigation Network Zone 3	21	12-Jan-26	04-Feb-26	20-Jan-26 A	13-Dec-26	$297,889.13
Zone 2		84	14-Jan-26	09-Apr-26	14-Jan-26 A	15-Dec-26	5,782,474.4
A103640	Testing and Commissioning for Sewerage Network Zone 2	21	05-Mar-26	09-Apr-26	05-Mar-26 A	15-Dec-26	$700,557.00
A103650	Testing and Commissioning for Rain Water Drainage Network Zone 2	21	19-Jan-26	11-Feb-26	11-Apr-26 A	17-Nov-26	3,578,003.3
A103660	Testing and Commissioning for Potable Water Network Zone 2	21	14-Jan-26	07-Feb-26	14-Jan-26 A	02-Dec-26	$908,135.90
A103670	Testing and Commissioning for Irrigation Network Zone 2	21	19-Jan-26	11-Feb-26	10-Feb-26 A	15-Nov-26	$595,778.27
Zone 1		86	18-Jan-26	25-Mar-26	18-Jan-26 A	26-Dec-26	5,782,474.4
A103690	Testing and Commissioning for Sewerage Network Zone 1	21	11-Feb-26	25-Mar-26	11-Feb-26 A	26-Dec-26	$700,557.00
A103700	Testing and Commissioning for Rain Water Drainage Network Zone 1	21	19-Jan-26	11-Feb-26	19-Jan-26 A	09-Nov-26	3,578,003.3
A103710	Testing and Commissioning for Potable Water Network Zone 1	21	18-Jan-26	10-Feb-26	18-Jan-26 A	06-Dec-26	$908,135.90
A103720	Testing and Commissioning for Irrigation Network Zone 1	21	19-Jan-26	11-Feb-26	19-Jan-26 A	17-Nov-26	$595,778.27
General		21	20-Apr-27	18-May-27	14-Jun-26 A	08-May-27	2,887,267.6
A103630	Testing and Commissioning for Communication	21	20-Apr-27	18-May-27	14-Jun-26 A	08-May-27	2,887,267.6

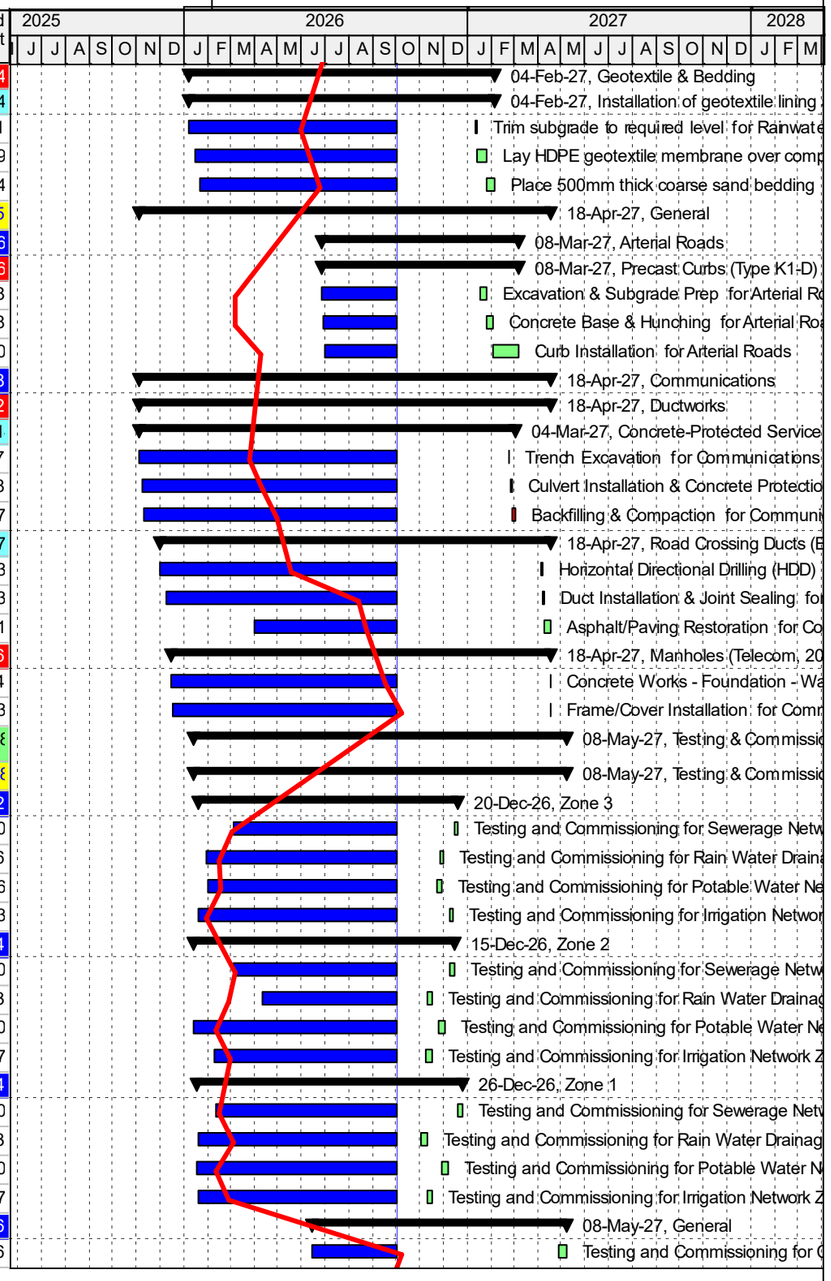

Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary

TASK filter: 2 Weeks Ahead.

© Oracle Corporation
