
Development of Phase One – Part Two – Third Industrial

Activity ID	Activity Name	Original Duration	BL Project Start	BL Project Finish	Start	Finish	Budgeted Total Cost	Earned Value Cost	Schedule % Complete	Performance % Complete
	Development of Phase One – Part Two – Third Industrial City in Dammam - 01-C	889	19-May-25	18-May-27	19-May-25 A	24-Oct-27	),776,076.78	6,730,386.15	88.47%	75.6%
	Milestones	889	19-May-25	18-May-27	19-May-25 A	24-Oct-27	$0.00	$0.00	0%	0%
	Mobilization	583	19-May-25	13-Aug-25	19-May-25 A	22-Dec-26	$0.00	$0.00	0%	0%
	Mobilization	30	19-May-25	17-Jun-25	19-May-25 A	25-Jun-25 A	$0.00	$0.00	0%	0%
	Deliverables	473	19-May-25	13-Aug-25	19-May-25 A	22-Dec-26	$0.00	$0.00	0%	0%
	Submittals	463	19-May-25	02-Aug-25	19-May-25 A	10-Dec-26	$0.00	$0.00	0%	0%
	Approvals	463	31-May-25	13-Aug-25	19-May-25 A	22-Dec-26	$0.00	$0.00	0%	0%
	Engineering	401	19-May-25	08-Nov-26	20-May-25 A	14-Oct-26	7,013,282.3	6,869,101.7	98.52%	97.94%
	Shop Drawing	273	19-May-25	16-Jul-25	20-May-25 A	08-Oct-26	$0.00	$0.00	0%	0%
	Submittals	207	19-May-25	02-Jul-25	20-May-25 A	01-Apr-26 A	$0.00	$0.00	0%	0%
	Approvals	240	03-Jul-25	16-Jul-25	06-Jul-25 A	08-Oct-26	$0.00	$0.00	0%	0%
	Material Submittal & Approval	368	22-Jun-25	08-Nov-26	26-May-25 A	14-Oct-26	7,013,282.3	6,869,101.7	98.52%	97.94%
	Long Lead Items	178	22-Jun-25	19-Feb-26	18-Jun-25 A	07-Oct-26	2,869,511.8	2,807,204.8	100%	97.83%
	Pipes (DI / GRP) - For potable, irrigation, sewer, storm	18	03-Jul-25	28-Jul-25	18-Jun-25 A	22-Jul-25 A	$179,398.95	$179,398.95	100%	100%
	Drainage Channel Covers (GRP / DI) - For storm and wastewater	24	03-Jul-25	05-Aug-25	18-Jun-25 A	24-Jul-25 A	1,308,857.0	1,308,857.0	100%	100%
	Manholes (Precast / Cast in situ) - All networks	20	03-Jul-25	30-Jul-25	20-Jul-25 A	29-Jul-25 A	$356,500.61	$356,500.61	100%	100%
	Control & Instrumentation Devices - Flow meters, pressure sensors	20	03-Jul-25	30-Jul-25	20-Jul-25 A	02-Sep-25 A	$46,453.40	$46,453.40	100%	100%
	Pumps (Sewage, Irrigation, Booster) - Especially for pumping stations	54	22-Jun-25	17-Jul-25	12-Aug-25 A	16-Oct-25 A	$525,232.91	$525,232.91	100%	100%
	Lighting Poles & Fixtures - External works, Roads, PS	20	03-Jul-25	30-Jul-25	03-Jul-25 A	07-Aug-25 A	$90,001.15	$90,001.15	100%	100%
	Generators & Fuel Tanks - PS & Control Bldg backup power	128	03-Jul-25	30-Jul-25	20-Jul-25 A	07-Oct-26	$311,534.63	$249,227.70	100%	80%
	Cable Trays / Electrical Panels (MCC) - PS and Control Buildings	33	22-Jan-26	19-Feb-26	20-Jul-25 A	24-Aug-25 A	$11,656.73	$11,656.73	100%	100%
	Odor Control Units - Sewer PS-specific	20	16-Nov-25	11-Dec-25	22-Jul-25 A	13-Aug-25 A	$39,876.38	$39,876.38	100%	100%
	Short Lead Items	368	03-Jul-25	08-Nov-26	26-May-25 A	14-Oct-26	4,143,770.5	4,061,896.8	97.5%	98.02%
	Asphalt	47	11-Oct-26	08-Nov-26	05-Aug-25 A	21-Sep-25 A	$103,594.66	$103,594.66	0%	100%
	Pipes (HDPE / uPVC) - For potable, irrigation, sewer, storm	20	03-Jul-25	30-Jul-25	26-May-25 A	24-Jun-25 A	1,496,527.7	1,496,527.7	100%	100%
	Valves (Gate, Air, NRV, Flow Control) - All water & drainage systems	20	03-Jul-25	30-Jul-25	03-Jul-25 A	02-May-26 A	$123,222.89	$123,222.89	100%	100%
	Chambers (Valve / Flowmeter / Washout) - Sewer, Potable, Irrigation	20	03-Jul-25	30-Jul-25	15-Jul-25 A	05-Aug-25 A	$284,016.32	$284,016.32	100%	100%
	Communication Ducts & Manholes - Telecom systems	20	03-Jun-26	01-Jul-26	16-Jul-25 A	03-Aug-25 A	$64,045.09	$64,045.09	100%	100%
	Air Vents / Washout Assemblies - Water networks	76	03-Jul-25	14-Aug-25	17-Jul-25 A	02-Oct-25 A	$36,002.07	$36,002.07	100%	100%
	Warning Tapes, Marker Posts - All underground works	36	03-Jul-25	30-Jul-25	01-Sep-25 A	01-Sep-25 A	$0.00	$0.00	0%	0%
	Concrete (for culverts, pads, plinths) - Structural support works	31	03-Jul-25	14-Aug-25	27-Jul-25 A	07-Aug-25 A	1,207,542.1	1,207,542.1	100%	100%
	Steel (Rebar, Gratings, Ladders, Covers) - Structural & drainage items	20	03-Jul-25	30-Jul-25	05-Jul-25 A	16-Jul-25 A	$524,731.72	$524,731.72	100%	100%
	Interlock Tiles / Curbstone - Roads, Sidewalks, Landscape	20	01-Feb-26	03-Mar-26	01-Feb-26 A	13-Oct-26	$40,886.85	$32,709.48	100%	80%
	Landscaping Materials (Soil, Plants) - Final works, softscape	63	01-Feb-26	03-Mar-26	13-Aug-25 A	14-Oct-26	$263,201.00	$189,504.72	100%	72%
	Procurement	565	19-May-25	25-Jan-27	19-May-25 A	01-Feb-27	13,038,834.7	11,076,553.6	96.09%	95.44%
	Prequalification	462	19-May-25	11-Oct-26	19-May-25 A	07-Oct-26	$0.00	$0.00	0%	0%
	Long Lead Items	282	19-May-25	21-Jan-26	19-May-25 A	26-Dec-25 A	$0.00	$0.00	0%	0%
	Pipes (DI / GRP) - For potable, irrigation, sewer, storm	34	19-May-25	02-Jul-25	19-May-25 A	24-Jun-25 A	$0.00	$0.00	0%	0%
	Drainage Channel Covers (GRP / DI) - For storm and wastewater	34	19-May-25	02-Jul-25	19-May-25 A	24-Jun-25 A	$0.00	$0.00	0%	0%
	Manholes (Precast / Cast in situ) - All networks	34	19-May-25	02-Jul-25	19-May-25 A	30-Jul-25 A	$0.00	$0.00	0%	0%
	Control & Instrumentation Devices - Flow meters, pressure sensors	34	19-May-25	02-Jul-25	19-May-25 A	30-Jul-25 A	$0.00	$0.00	0%	0%
	Pumps (Sewage, Irrigation, Booster) - Especially for pumping stations	34	19-May-25	02-Jul-25	18-Oct-25 A	19-Oct-25 A	$0.00	$0.00	0%	0%
	Lighting Poles & Fixtures - External works, Roads, PS	34	19-May-25	02-Jul-25	19-May-25 A	02-Aug-25 A	$0.00	$0.00	0%	0%
	Generators & Fuel Tanks - PS & Control Bldg backup power	34	19-May-25	02-Jul-25	19-May-25 A	02-Aug-25 A	$0.00	$0.00	0%	0%
	Cable Trays / Electrical Panels (MCC) - PS and Control Buildings	34	14-Dec-25	21-Jan-26	26-Sep-25 A	26-Dec-25 A	$0.00	$0.00	0%	0%
	Odor Control Units - Sewer PS-specific	31	09-Oct-25	13-Nov-25	05-Aug-25 A	09-Sep-25 A	$0.00	$0.00	0%	0%
	Short Lead Items	462	19-May-25	11-Oct-26	19-May-25 A	07-Oct-26	$0.00	$0.00	0%	0%
	Asphalt	85	31-Aug-26	11-Oct-26	17-Jul-25 A	09-Sep-25 A	$0.00	$0.00	0%	0%
	Pipes (HDPE / uPVC) - For potable, irrigation, sewer, storm	34	19-May-25	02-Jul-25	19-May-25 A	24-Jun-25 A	$0.00	$0.00	0%	0%
	Valves (Gate, Air, NRV, Flow Control) - All water & drainage systems	34	19-May-25	02-Jul-25	19-May-25 A	03-Aug-25 A	$0.00	$0.00	0%	0%
	Chambers (Valve / Flowmeter / Washout) - Sewer, Potable, Irrigation	34	19-May-25	02-Jul-25	19-May-25 A	03-Aug-25 A	$0.00	$0.00	0%	0%
	Communication Ducts & Manholes - Telecom systems	34	20-Apr-26	03-Jun-26	02-Aug-25 A	03-Aug-25 A	$0.00	$0.00	0%	0%

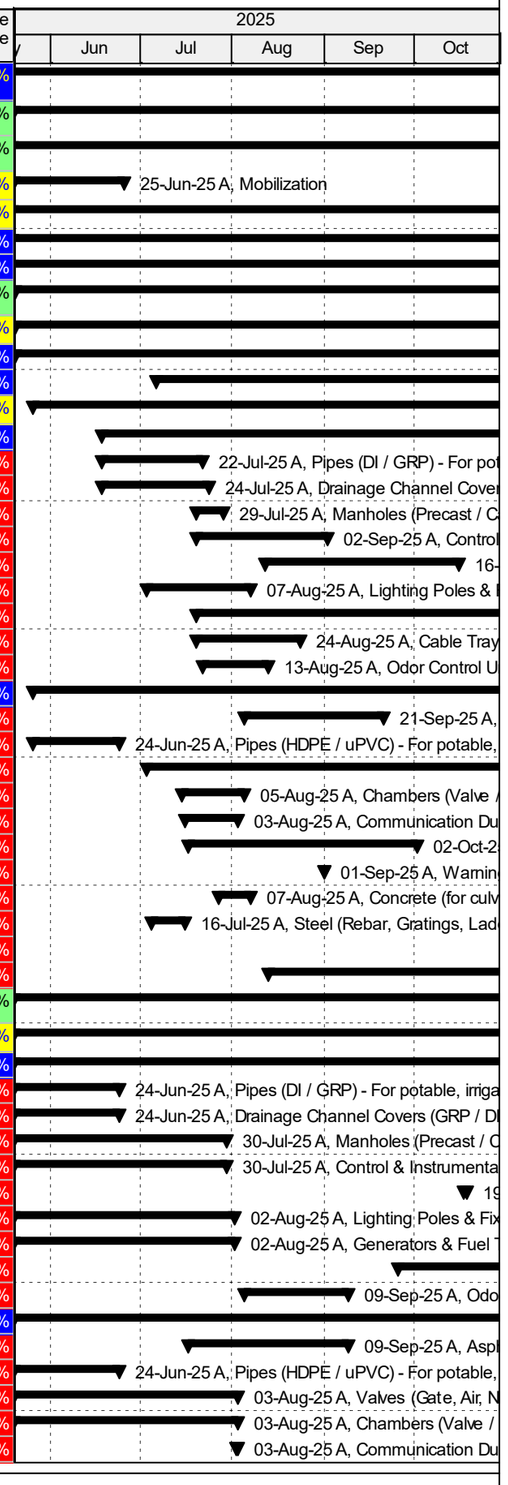

© Oracle Corporation

Development of Phase One – Part Two – Third Industrial

2026 | 2027 | 2028

Nov | Dec | Jan | Feb | Mar | Apr | May | Jun | Jul | Aug | Sep | Oct | Nov | Dec | Jan | Feb | Mar | Apr | May | Jun | Jul | Aug | Sep | Oct | Nov | Dec | Jan

24-Oct-27, Development of Phas
24-Oct-27, Milestones
22-Dec-26, Mobilization
22-Dec-26, Deliverables
10-Dec-26, Submittals
22-Dec-26, Approvals
14-Oct-26, Engineering
08-Oct-26, Shop Drawing
01-Apr-26 A, Submittals
08-Oct-26, Approvals
14-Oct-26, Material Submittal & Approval
07-Oct-26, Long Lead Items
able, irrigation, sewer, storm
s (GRP / DI) - For storm and wastewater
ast in situ) - All networks
& Instrumentation Devices - Flow meters, pressure sensors
Oct-25 A, Pumps (Sewage, Irrigation, Booster) - Especially for pumping stations
ixtures - External works, Roads, PS
07-Oct-26, Generators & Fuel Tanks - PS & Control Bldg backup power
s / Electrical Panels (MCC) - PS and Control Buildings
nits - Sewer PS-specific
14-Oct-26, Short Lead Items
Asphalt
irrigation, sewer, storm
02-May-26 A, Valves (Gate, Air, NRV, Flow Control) - All water & drainage systems
Flowmeter / Washout) - Sewer, Potable, Irrigation
cts & Manholes - Telecom systems
5 A, Air Vents / Washout Assemblies - Water networks
g Tapes, Marker Posts - All underground works
erts, pads, plinths) - Structural support works
ders, Covers) - Structural & drainage items
13-Oct-26, Interlock Tiles / Curbstone - Roads, Sidewalks, Landscape
14-Oct-26, Landscaping Materials (Soil, Plants) - Final works, softscape
01-Feb-27, Procurement
07-Oct-26, Prequalification
26-Dec-25 A, Long Lead Items
tion, sewer, storm
) - For storm and wastewater
ast in situ) - All networks
tion Devices - Flow meters, pressure sensors
-Oct-25 A, Pumps (Sewage, Irrigation, Booster) - Especially for pumping stations
tures - External works, Roads, PS
anks - PS & Control Bldg backup power
26-Dec-25 A, Cable Trays / Electrical Panels (MCC) - PS and Control Buildings
Control Units - Sewer PS-specific
07-Oct-26, Short Lead Items
halt
irrigation, sewer, storm
RV, Flow Control) - All water & drainage systems
Flowmeter / Washout) - Sewer, Potable, Irrigation
cts & Manholes - Telecom systems


Actual Level of Effort | Remaining Work | Milestone
Actual Work | Critical Remaining Work | summary

TASK filter: All Activities

© Oracle Corporation

Development of Phase One – Part Two – Third Industrial

Activity ID	Activity Name	Original Duration	BL Project Start	BL Project Finish	Start	Finish	Budgeted Total Cost	Earned Value Cost	Schedule % Complete	Performance % Complete
	Air Vents / Washout Assemblies - Water networks	34	19-May-25	02-Jul-25	19-May-25 A	03-Aug-25 A	$0.00	$0.00	0%	0%
	Warning Tapes, Marker Posts - All underground works	34	19-May-25	02-Jul-25	18-Jul-25 A	25-Sep-25 A	$0.00	$0.00	0%	0%
	Concrete (for culverts, pads, plinths) - Structural support works	34	19-May-25	02-Jul-25	19-May-25 A	24-Jun-25 A	$0.00	$0.00	0%	0%
	Steel (Rebar, Gratings, Ladders, Covers) - Structural & drainage items	34	19-May-25	02-Jul-25	19-May-25 A	14-Jul-25 A	$0.00	$0.00	0%	0%
	Interlock Tiles / Curbstone - Roads, Sidewalks, Landscape	34	22-Dec-25	29-Jan-26	21-Feb-26 A	07-Oct-26	$0.00	$0.00	0%	0%
	Landscaping Materials (Soil, Plants) - Final works, softscape	34	22-Dec-25	29-Jan-26	13-Aug-25 A	07-Oct-26	$0.00	$0.00	0%	0%
	Long Lead Items	426	19-Jul-25	07-Nov-26	02-Aug-25 A	30-Nov-26	17,609,507.(	17,271,293.9	99.99%	98.08%
	Pipes (DI / GRP) - For potable, irrigation, sewer, storm	163	29-Jul-25	22-Nov-25	02-Aug-25 A	06-Jan-26 A	1,100,928.4	1,100,928.4	100%	100%
	Drainage Channel Covers (GRP / DI) - For storm and wastewater	157	06-Aug-25	04-Jan-26	05-Nov-25 A	04-Oct-26	8,032,142.3	7,951,820.9	100%	99%
	Manholes (Precast / Cast in situ) - All networks	213	31-Jul-25	17-Dec-25	16-Sep-25 A	21-May-26 A	2,187,758.8	2,187,758.8	100%	100%
	Control & Instrumentation Devices - Flow meters, pressure sensors	285	31-Jul-25	17-Dec-25	24-Aug-25 A	29-Oct-26	$285,073.41	$270,819.74	100%	95%
	Pumps (Sewage, Irrigation, Booster) - Especially for pumping stations	160	19-Jul-25	16-Dec-25	16-Oct-25 A	07-Oct-26	3,223,228.6	3,094,299.5	100%	96%
	Lighting Poles & Fixtures - External works, Roads, PS	117	31-Jul-25	23-Dec-25	10-Oct-25 A	12-Jan-26 A	$552,315.51	$552,315.51	100%	100%
	Generators & Fuel Tanks - PS & Control Bldg backup power	193	31-Jul-25	13-Dec-25	05-Dec-25 A	26-Oct-26	1,911,813.4	1,797,104.6	100%	94%
	Cable Trays / Electrical Panels (MCC) - PS and Control Buildings	218	19-Feb-26	07-Nov-26	24-Aug-25 A	23-Oct-25 A	$71,534.55	$71,534.55	98.33%	100%
	Odor Control Units - Sewer PS-specific	297	14-Dec-25	31-Aug-26	09-Nov-25 A	30-Nov-26	$244,711.80	$244,711.80	100%	100%
	Short Lead Items	507	31-Jul-25	25-Jan-27	25-Jul-25 A	01-Feb-27	25,429,327.6	23,805,259.6	93.38%	93.61%
	Asphalt	71	08-Nov-26	25-Jan-27	19-Nov-25 A	01-Dec-26	$635,735.66	$629,378.30	0%	99%
	Pipes (HDPE / uPVC) - For potable, irrigation, sewer, storm	174	31-Jul-25	06-Nov-25	01-Aug-25 A	14-Jan-26 A	9,183,832.7	9,183,832.7	100%	100%
	Valves (Gate, Air, NRV, Flow Control) - All water & drainage systems	148	31-Jul-25	06-Dec-25	25-Nov-25 A	13-Apr-26 A	$756,189.36	$756,189.36	100%	100%
	Chambers (Valve / Flowmeter / Washout) - Sewer, Potable, Irrigation	140	31-Jul-25	18-Nov-25	10-Nov-25 A	31-Mar-26 A	1,742,940.1	1,742,940.1	100%	100%
	Communication Ducts & Manholes - Telecom systems	104	31-Aug-26	06-Jan-27	24-Aug-25 A	16-Jan-27 A	$393,029.41	$393,029.41	0%	100%
	Air Vents / Washout Assemblies - Water networks	136	16-Aug-25	21-Dec-25	13-Dec-25 A	12-May-26 A	$220,936.06	$220,936.06	100%	100%
	Warning Tapes, Marker Posts - All underground works	93	31-Jul-25	26-Oct-25	30-Sep-25 A	15-Dec-25 A	$0.00	$0.00	0%	0%
	Concrete (for culverts, pads, plinths) - Structural support works	273	16-Aug-25	08-Nov-26	30-Jul-25 A	15-Jun-26 A	7,410,396.9	7,410,396.9	91.17%	100%
	Steel (Rebar, Gratings, Ladders, Covers) - Structural & drainage items	254	31-Jul-25	12-Oct-25	25-Jul-25 A	17-Jun-26 A	3,220,152.9	3,220,152.9	100%	100%
	Interlock Tiles / Curbstone - Roads, Sidewalks, Landscape	90	03-Mar-26	07-Jul-26	03-Nov-25 A	02-Nov-26	$250,912.80	$248,403.67	100%	99%
	Landscaping Materials (Soil, Plants) - Final works, softscape	94	03-Mar-26	07-Jul-26	14-Oct-26	01-Feb-27	1,615,201.5	$0.00	100%	0%
	Construction	884	19-May-25	18-May-27	19-May-25 A	19-Oct-27	60,346,352.	16,355,189.3	89.87%	72.56%
	Zone 3	537	13-Oct-25	26-Dec-26	15-Sep-25 A	30-Jun-27	30,801,187.7	32,697,137.4	97.32%	64.36%
	Sewerage Network Zone 3	383	13-Oct-25	26-Dec-26	01-Jan-26 A	17-Apr-27	6,994,093.4	2,013,913.9	84.12%	28.79%
	Pipework: Supply, Installation, and Testing	213	19-Oct-25	27-Jan-26	01-Jan-26 A	26-Oct-26	$369,724.94	$353,055.57	100%	95.49%
	UPVC Pipes Installation (150mm–315mm)	71	19-Oct-25	12-Jan-26	01-Apr-26 A	09-May-26 A	$182,970.73	$182,970.73	100%	100%
	GRP Pipes Installation (400mm–700mm)	94	19-Oct-25	27-Jan-26	16-Apr-26 A	23-May-26 A	$82,570.64	$82,570.64	100%	100%
	HDPE Pressure Pipes Installation (250mm–630mm)	213	19-Oct-25	27-Jan-26	01-Jan-26 A	26-Oct-26	$104,183.57	$87,514.20	100%	84%
	Fittings and Valves	27	14-Dec-25	13-Jan-26	03-Oct-26	02-Nov-26	$30,711.20	$0.00	100%	0%
	Valve & Flow Meter Chambers	87	19-Oct-25	10-Feb-26	08-Jun-26 A	14-Dec-26	$49,924.39	$17,953.74	100%	35.96%
	Valve Chambers Construction	58	19-Oct-25	04-Jan-26	08-Jun-26 A	16-Nov-26	$6,894.06	$2,861.04	100%	41.5%
	Water Drain Chambers Construction	75	19-Oct-25	23-Jan-26	16-Jun-26 A	03-Dec-26	$22,394.28	$8,733.77	100%	39%
	Discharge Chambers Construction	82	19-Oct-25	05-Feb-26	01-Jul-26 A	09-Dec-26	$15,643.62	$5,709.92	100%	36.5%
	Flow Meter Chambers Construction	87	19-Oct-25	10-Feb-26	14-Jul-26 A	14-Dec-26	$4,992.44	$649.02	100%	13%
	Manholes	213	19-Oct-25	04-Mar-26	01-Jan-26 A	03-Dec-26	$849,279.83	$642,540.77	100%	75.66%
	1200mm GRP Manholes with Backdrop	93	19-Oct-25	19-Jan-26	01-Jan-26 A	13-Feb-26 A	$422,629.13	$422,629.13	100%	100%
	1500mm GRP Manholes (Standard & Backdrop)	161	19-Oct-25	09-Feb-26	02-Feb-26 A	20-Nov-26	$400,264.86	$208,137.73	100%	52%
	1800mm GRP Manholes (Standard & Backdrop)	168	19-Oct-25	26-Feb-26	17-Feb-26 A	27-Nov-26	$19,968.17	$10,383.45	100%	52%
	2000mm GRP Manholes (Standard & Backdrop)	174	19-Oct-25	04-Mar-26	15-Feb-26 A	03-Dec-26	$6,323.52	$1,296.32	100%	20.5%
	Pumping Stations	253	13-Oct-25	26-Dec-26	13-Jan-26 A	17-Apr-27	5,694,453.0	1,000,363.8	80.5%	17.57%
	Perimeter Walls & Gates	65	13-Oct-25	11-Dec-25	04-May-26 A	07-Sep-26 A	$369,469.83	$369,469.83	100%	100%
	Sewage Pumps and MCC System	42	08-Nov-26	26-Dec-26	26-Oct-26	14-Dec-26	$991,481.15	$0.00	0%	0%
	Odor Control System	46	31-Aug-26	25-Oct-26	01-Aug-26 A	17-Sep-26 A	$276,510.51	$276,510.51	56.96%	100%
	In-Line Booster Stations	63	01-Dec-25	11-Feb-26	03-Oct-26	14-Dec-26	1,968,220.0	$0.00	100%	0%
	Engine/Motor Control Center Buildings	8	06-Nov-25	08-Dec-25	03-Oct-26	11-Oct-26	$45,941.19	$0.00	100%	0%
	Valves and Fittings (General Supply & Installation)	8	18-Dec-25	27-Dec-25	30-Aug-26 A	05-Nov-26	$43,723.31	$8,744.66	100%	20%
	Tank with Canopy	12	28-Dec-25	10-Jan-26	05-Nov-26	19-Nov-26	$720,080.25	$0.00	100%	0%

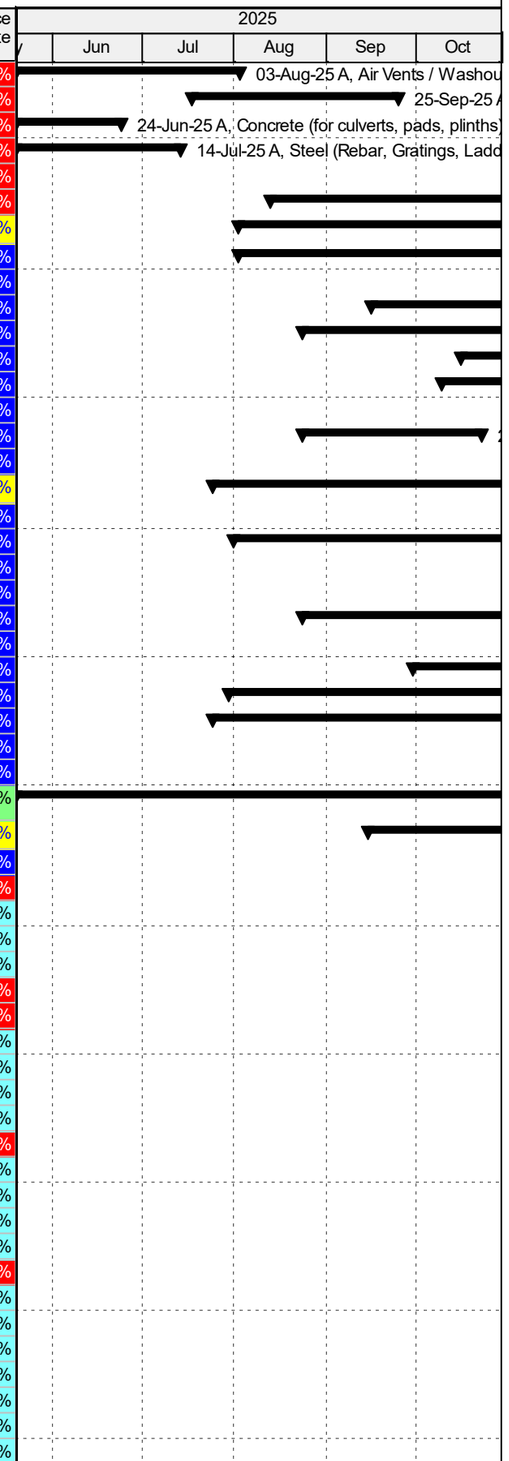

© Oracle Corporation

Development of Phase One – Part Two – Third Industrial

2026 | 2027 | 2028

Nov | Dec | Jan | Feb | Mar | Apr | May | Jun | Jul | Aug | Sep | Oct | Nov | Dec | Jan | Feb | Mar | Apr | May | Jun | Jul | Aug | Sep | Oct | Nov | Dec | Jan

t Assemblies - Water networks
, Warning Tapes, Marker Posts - All underground works
- Structural support works
ers, Covers) - Structural & drainage items
07-Oct-26, Interlock Tiles / Curbstone - Roads, Sidewalks, Landscape
07-Oct-26, Landscaping Materials (Soil, Plants) - Final works, softscape
30-Nov-26, Long Lead Items
06-Jan-26 A, Pipes (DI / GRP) - For potable, irrigation, sewer, storm
04-Oct-26, Drainage Channel Covers (GRP / DI) - For storm and wastewater
21-May-26 A, Manholes (Precast / Cast in situ) - All networks
29-Oct-26, Control & Instrumentation Devices - Flow meters, pressure sensors
07-Oct-26, Pumps (Sewage, Irrigation, Booster) - Especially for pumping stations
12-Jan-26 A, Lighting Poles & Fixtures - External works, Roads, PS
26-Oct-26, Generators & Fuel Tanks - PS & Control Bldg backup power
23-Oct-25 A, Cable Trays / Electrical Panels (MCC) - PS and Control Buildings
30-Nov-26, Odor Control Units - Sewer PS-specific
01-Feb-27, Short Lead Items
01-Dec-26, Asphalt
14-Jan-26 A, Pipes (HDPE / uPVC) - For potable, irrigation, sewer, storm
13-Apr-26 A, Valves (Gate, Air, NRV, Flow Control) - All water & drainage systems
31-Mar-26 A, Chambers (Valve / Flowmeter / Washout) - Sewer, Potable, Irrigation
16-Jan-27 A, Communication Ducts & Manholes - Telecom systems
12-May-26 A, Air Vents / Washout Assemblies - Water networks
15-Dec-25 A, Warning Tapes, Marker Posts - All underground works
15-Jun-26 A, Concrete (for culverts, pads, plinths) - Structural support works
17-Jun-26 A, Steel (Rebar, Gratings, Ladders, Covers) - Structural & drainage items
02-Nov-26, Interlock Tiles / Curbstone - Roads, Sidewalks, Landscape
01-Feb-27, Landscaping Materials (Soil, Plants) - Final works, softscape
19-Oct-27, Construction
30-Jun-27, Zone 3
17-Apr-27, Sewerage Network Zone 3
26-Oct-26, Pipework: Supply, Installation, and Testing
09-May-26 A, UPVC Pipes Installation (150mm–315mm)
23-May-26 A, GRP Pipes Installation (400mm–700mm)
26-Oct-26, HDPE Pressure Pipes Installation (250mm–630mm)
02-Nov-26, Fittings and Valves
14-Dec-26, Valve & Flow Meter Chambers
16-Nov-26, Valve Chambers Construction
03-Dec-26, Water Drain Chambers Construction
09-Dec-26, Discharge Chambers Construction
14-Dec-26, Flow Meter Chambers Construction
03-Dec-26, Manholes
13-Feb-26 A, 1200mm GRP Manholes with Backdrop
20-Nov-26, 1500mm GRP Manholes (Standard & Backdrop)
27-Nov-26, 1800mm GRP Manholes (Standard & Backdrop)
03-Dec-26, 2000mm GRP Manholes (Standard & Backdrop)
17-Apr-27, Pumping Stations
07-Sep-26 A, Perimeter Walls & Gates
14-Dec-26, Sewage Pumps and MCC System
17-Sep-26 A, Odor Control System
14-Dec-26, In-Line Booster Stations
11-Oct-26, Engine/Motor Control Center Buildings
05-Nov-26, Valves and Fittings (General Supply & Installation)
19-Nov-26, Tank with Canopy

Actual Level of Effort | Remaining Work | Milestone
Actual Work | Critical Remaining Work | summary

TASK filter: All Activities

© Oracle Corporation

Development of Phase One – Part Two – Third Industrial

Activity ID	Activity Name	Original Duration	BL Project Start	BL Project Finish	Start	Finish	Budgeted Total Cost	Earned Value Cost	Schedule % Complete	Performance % Complete
	Pump Well and Valve Chambers	77	11-Jan-26	14-May-26	19-Nov-26	27-Feb-27	$773,616.05	$0.00	100%	0%
	Odor Control System Base/Plinth	6	03-Jun-26	10-Jun-26	08-Apr-27	15-Apr-27	$16,590.51	$0.00	100%	0%
	Lighting Works	13	10-Jun-26	25-Jun-26	13-Jan-26 A	17-Apr-27	$384,043.12	$345,638.81	100%	90%
	Duct Works	7	28-Apr-26	06-May-26	27-Feb-27	16-Mar-27	$15,220.07	$0.00	100%	0%
	Grounding Works	3	06-May-26	10-May-26	16-Mar-27	20-Mar-27	$7,603.32	$0.00	100%	0%
	Landscaping / Interlocking Tiles	21	10-May-26	08-Jun-26	20-Mar-27	13-Apr-27	$61,674.68	$0.00	100%	0%
	Pumping Station Internal Drainage Network	7	10-May-26	18-May-26	20-Mar-27	28-Mar-27	$20,278.98	$0.00	100%	0%
	Rainwater Drainage Network Zone 3	286	19-Oct-25	18-Jan-26	05-Jan-26 A	26-Nov-26	10,744,160.(	7,503,593.8:	100%	69.84%
	Pipe Laying Works	261	19-Oct-25	18-Jan-26	05-Jan-26 A	01-Nov-26	$591,302.61	$503,268.09	100%	85.11%
	Supply & Installation of uPVC Pipes (250–300mm dia)	153	19-Oct-25	13-Dec-25	05-Jan-26 A	09-Oct-26	$376,944.63	$329,826.55	100%	87.5%
	Supply & Installation of GRP Pipes (350–800mm dia)	253	19-Oct-25	18-Jan-26	05-Jan-26 A	23-Oct-26	$172,229.41	$146,395.00	100%	85%
	uPVC Connection Pipes (150mm dia)	261	19-Oct-25	05-Jan-26	05-Jan-26 A	01-Nov-26	$42,128.57	$27,046.54	100%	64.2%
	Precast Concrete Box Culverts	163	19-Oct-25	18-Jan-26	01-Mar-26 A	26-Nov-26	1,156,736.8	$441,213.10	100%	38.14%
	Box Culverts (500x500mm to 3500x800mm)	163	19-Oct-25	18-Jan-26	01-Mar-26 A	26-Nov-26	1,060,035.1	$344,511.41	100%	32.5%
	Tube Culverts at Road Intersections	34	15-Nov-25	07-Jan-26	01-Apr-26 A	12-May-26 A	$89,488.14	$89,488.14	100%	100%
	Box Culverts at Road Intersections	28	17-Nov-25	31-Dec-25	01-Apr-26 A	30-Apr-26 A	$7,213.55	$7,213.55	100%	100%
	Manholes	36	07-Dec-25	18-Jan-26	15-Oct-26	26-Nov-26	$780,038.12	$0.00	100%	0%
	Circular GRP Manholes (1200–1800mm dia)	32	07-Dec-25	13-Jan-26	15-Oct-26	22-Nov-26	$228,708.76	$0.00	100%	0%
	Concrete Manholes for 1500x1500 Box Pipes	32	07-Dec-25	13-Jan-26	15-Oct-26	22-Nov-26	$354,504.29	$0.00	100%	0%
	Concrete Manholes for 1000x1000 Box Pipes	36	07-Dec-25	18-Jan-26	15-Oct-26	26-Nov-26	$196,825.07	$0.00	100%	0%
	Chambers and Catch Basins	144	07-Dec-25	17-Jan-26	18-Jan-26 A	21-Oct-26	$607,967.93	$580,102.66	100%	95.42%
	Gully Outfalls	63	07-Dec-25	05-Jan-26	18-Jan-26 A	17-Oct-26	$179,065.55	$169,575.07	100%	94.7%
	Rainwater Catch Basins	121	07-Dec-25	10-Jan-26	08-Feb-26 A	15-Oct-26	$260,802.54	$259,237.73	100%	99.4%
	Precast Chambers for Absorption Pits	144	07-Dec-25	17-Jan-26	12-Feb-26 A	21-Oct-26	$168,099.84	$151,289.86	100%	90%
	Gully Outfalls to Swales	144	28-Dec-25	18-Jan-26	01-Feb-26 A	05-Nov-26	$176,898.27	$107,554.15	100%	60.8%
	Gully Outfalls to Swales	130	28-Dec-25	17-Jan-26	01-Feb-26 A	20-Oct-26	$141,518.62	$107,554.15	100%	76%
	Riprap Works & Protection	18	28-Dec-25	18-Jan-26	15-Oct-26	05-Nov-26	$35,379.65	$0.00	100%	0%
	Backfilling & Bedding	181	02-Nov-25	18-Jan-26	17-Mar-26 A	26-Oct-26	2,298,195.3	2,028,106.3:	100%	88.25%
	Backfilling Materials (Type A– 201–700mm Pipes)	142	02-Nov-25	05-Jan-26	17-Mar-26 A	04-Oct-26	1,533,378.5	1,488,910.5(	100%	97.1%
	Gravel Bedding & Filter Cloth for uPVC Drain Pipes	136	15-Nov-25	18-Jan-26	21-Mar-26 A	26-Oct-26	$764,816.78	$539,195.83	100%	70.5%
	Deep Basin for Groundwater Collection (2.5–3.0m)	153	10-Nov-25	18-Jan-26	02-Feb-26 A	26-Oct-26	5,133,020.9	3,843,349.4:	100%	74.88%
	Potable Water Network Zone 3	344	19-Oct-25	18-Jan-26	13-Oct-25 A	22-Dec-26	12,325,662.8	5,698,715.0	100%	46.23%
	Pipe Installation Works	85	19-Oct-25	14-Dec-25	01-Jan-26 A	13-Oct-26	1,002,366.1	$671,585.31	100%	67%
	Valve Installation & Chambers	111	09-Nov-25	18-Jan-26	02-Jun-26 A	27-Oct-26	$316,303.42	$245,261.67	100%	77.54%
	Flow Meter Installation	76	20-Nov-25	11-Jan-26	12-Aug-26 A	23-Nov-26	$61,536.16	$19,383.89	100%	31.5%
	Washout & Air Valve Chambers	44	09-Nov-25	03-Jan-26	01-Aug-26 A	12-Oct-26	$304,525.24	$238,753.17	100%	78.4%
	Pumping Station (Structure & Civil Works)	66	19-Oct-25	04-Jan-26	03-Oct-26	17-Dec-26	$473,145.06	$0.00	100%	0%
	Pump Station Building	31	30-Nov-25	05-Jan-26	14-Nov-26	19-Dec-26	$183,637.93	$0.00	100%	0%
	Pumping Equipment & Fire Systems	28	17-Dec-25	18-Jan-26	14-Nov-26	15-Dec-26	$946,290.12	$0.00	100%	0%
	Surge Protection	5	13-Jan-26	18-Jan-26	10-Dec-26	15-Dec-26	$28,227.66	$0.00	100%	0%
	Power & Generator System	12	03-Jan-26	15-Jan-26	30-Nov-26	13-Dec-26	2,851,518.7	$0.00	100%	0%
	Chlorination System	14	03-Jan-26	18-Jan-26	30-Nov-26	15-Dec-26	$518,457.97	$0.00	100%	0%
	Water Storage System	11	05-Jan-26	18-Jan-26	13-Oct-25 A	22-Dec-26	5,159,570.0	4,127,656.0	100%	80%
	Street Lighting	226	15-Dec-25	18-Jan-26	05-Dec-25 A	07-Dec-26	$480,084.41	$396,074.98	100%	82.5%
	Irrigation Network Zone 3	211	19-Oct-25	11-Jan-26	21-Mar-26 A	15-Nov-26	$832,623.82	$718,393.14	100%	86.28%
	Excavation, Pipe Laying & Backfilling	158	19-Oct-25	14-Dec-25	01-Apr-26 A	09-Oct-26	$546,284.50	$461,064.12	100%	84.4%
	Valves and Appurtenances	28	07-Dec-25	28-Dec-25	14-Jun-26 A	06-Oct-26	$63,598.84	$58,318.24	100%	91.7%
	Valve Rooms	28	11-Dec-25	01-Jan-26	01-May-26 A	03-Oct-26	$60,148.03	$59,696.92	100%	99.25%
	Washout Chambers	60	07-Dec-25	08-Jan-26	13-Apr-26 A	04-Oct-26	$70,306.78	$66,439.91	100%	94.5%
	Air Valve Chambers	27	07-Dec-25	06-Jan-26	21-Mar-26 A	03-Oct-26	$47,448.36	$47,092.49	100%	99.25%
	Flow Meter Chambers	159	07-Dec-25	11-Jan-26	01-Apr-26 A	15-Nov-26	$44,837.31	$25,781.45	100%	57.5%
	Rainwater Collection Ponds Zone 3	270	19-Jan-26	14-Nov-26	15-Sep-25 A	20-Mar-27	19,076,657.7	16,461,810.2	98.76%	86.29%
	Excavation for Rainwater Drainage Pond	226	19-Jan-26	14-Mar-26	01-Oct-25 A	09-Jan-27	$394,641.69	$325,776.71	100%	82.55%
	Deep excavation, backfill, disposal for pond formation	226	19-Jan-26	14-Mar-26	01-Oct-25 A	09-Jan-27	$394,641.69	$325,776.71	100%	82.55%


2025: Jun | Jul | Aug | Sep | Oct

Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary

TASK filter: All Activities

© Oracle Corporation

Development of Phase One – Part Two – Third Industrial

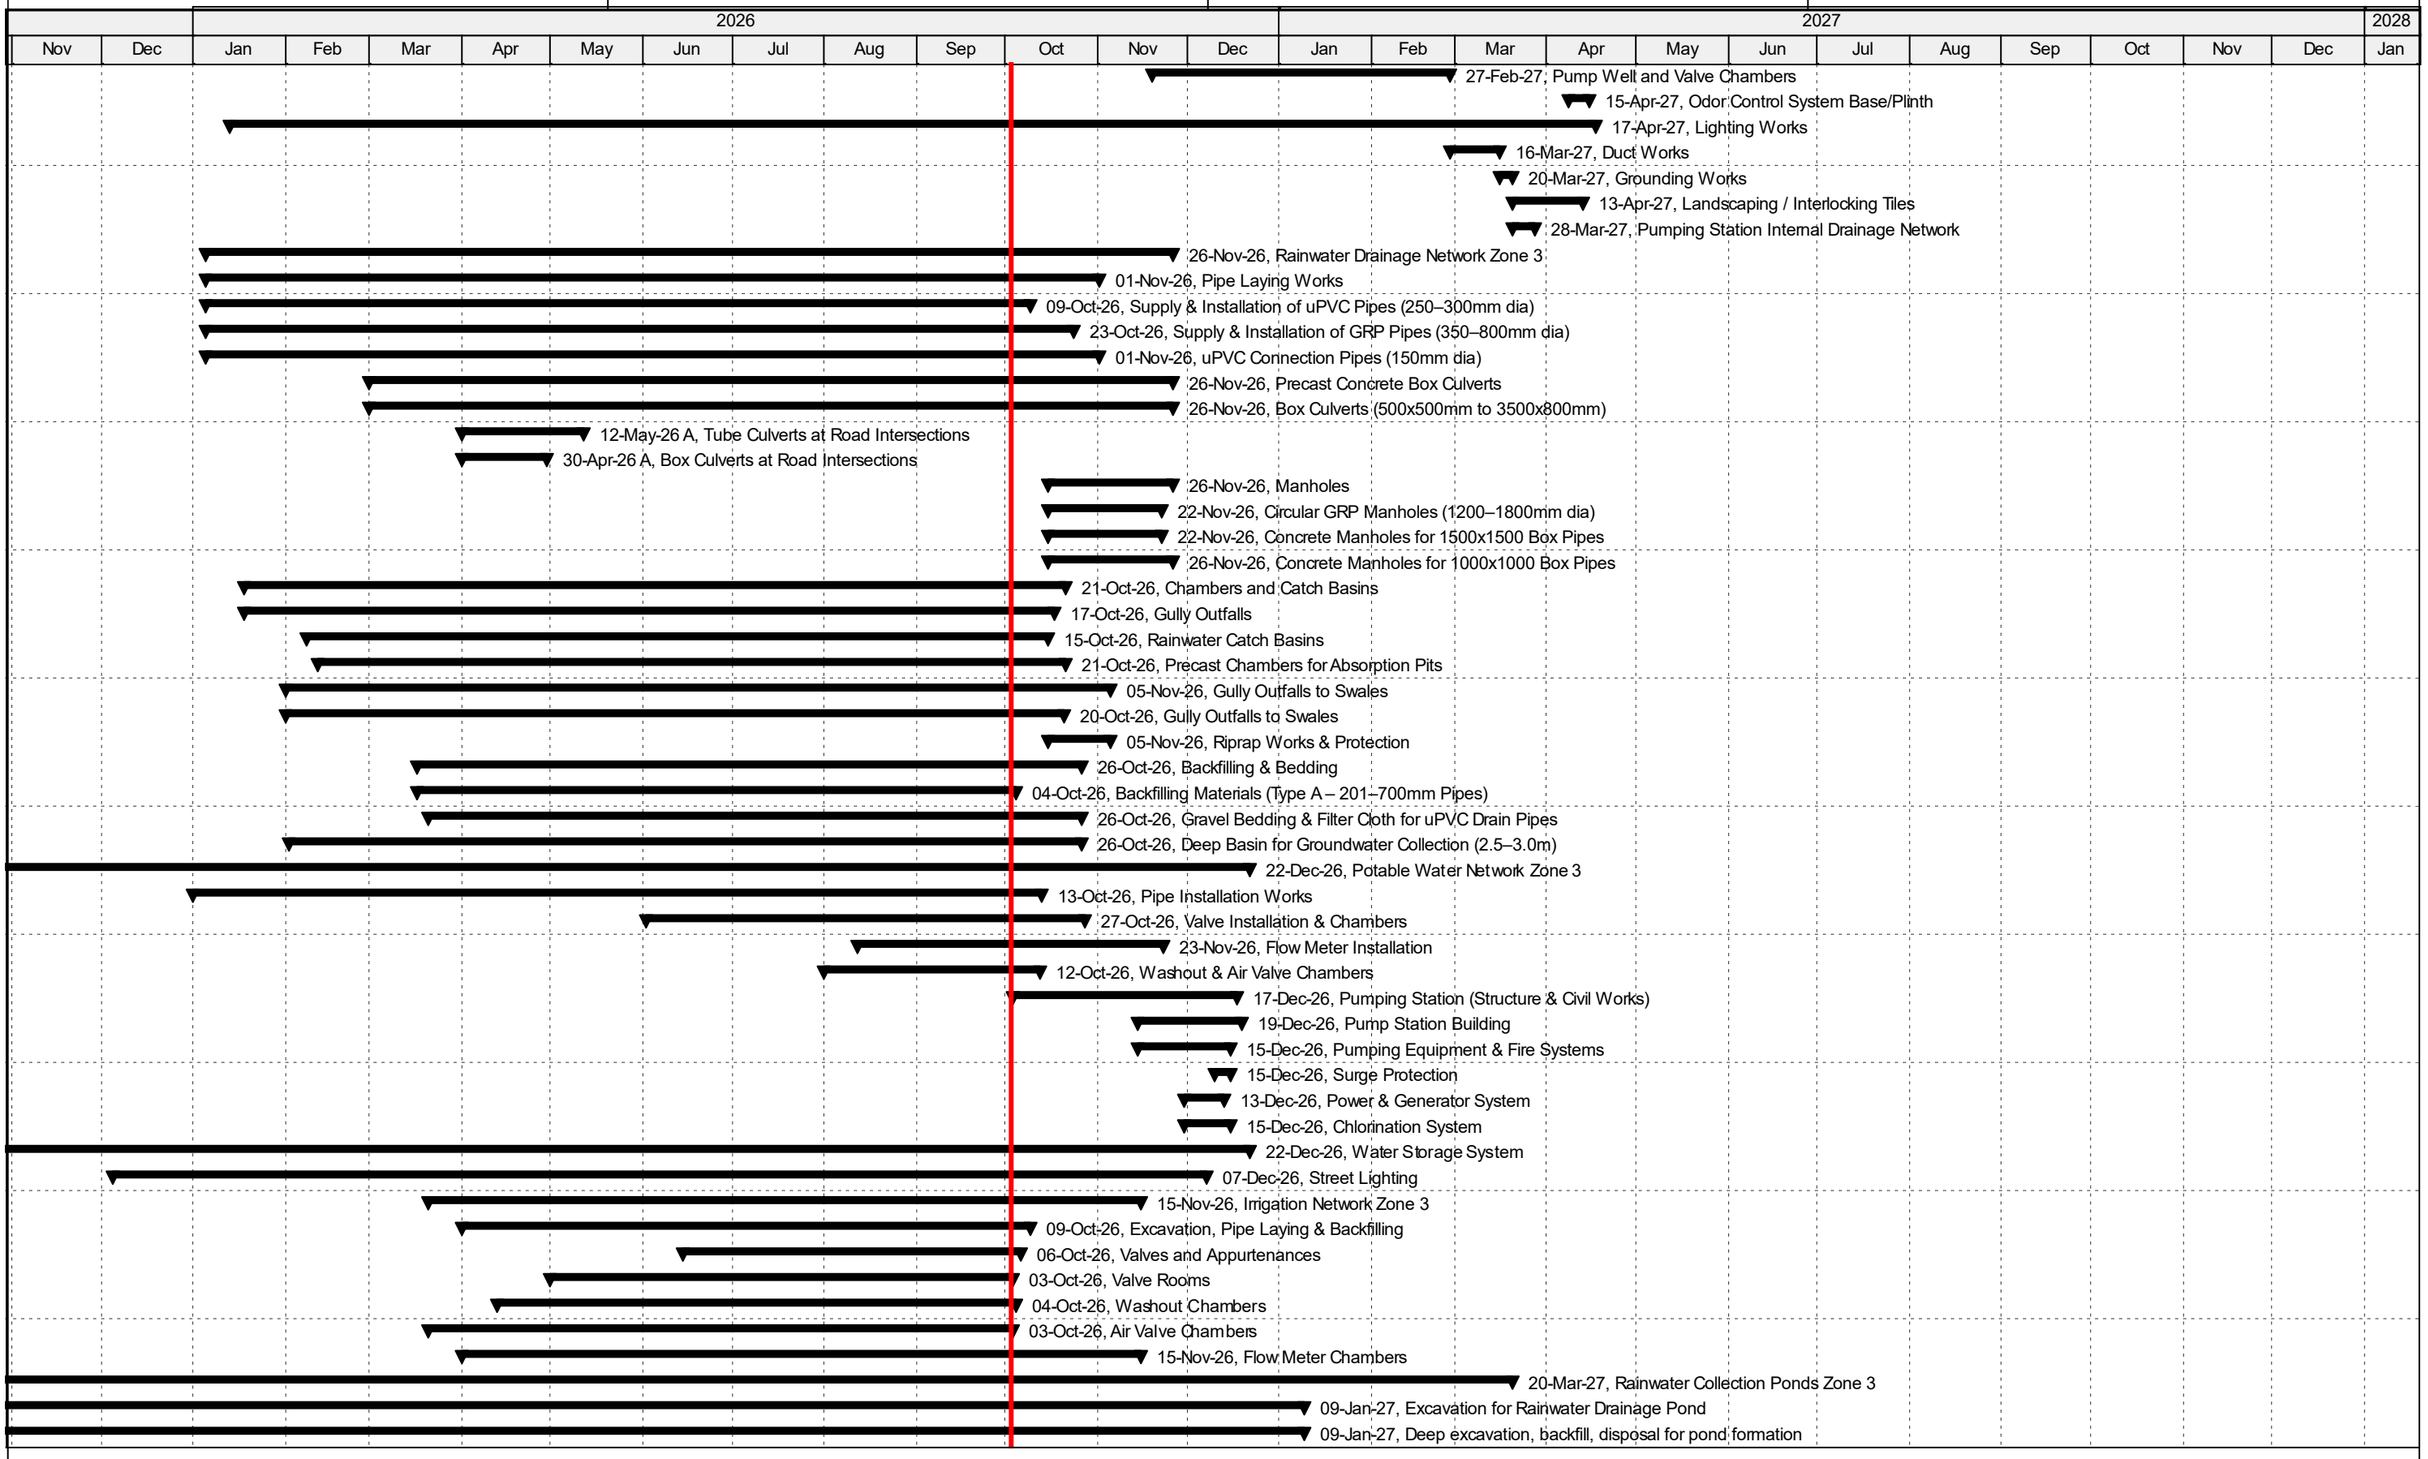

Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary

TASK filter: All Activities

© Oracle Corporation

Development of Phase One – Part Two – Third Industrial

Activity ID	Activity Name	Original Duration	BL Project Start	BL Project Finish	Start	Finish	Budgeted Total Cost	Earned Value Cost	Schedule % Complete	Performance % Complete
	General Site Preparation	39	22-Jan-26	10-May-26	15-Sep-25 A	05-Jan-27	15,134,572.8	13,717,975.2	100%	90.64%
	Backfilling Works	174	10-May-26	29-Jul-26	18-Nov-25 A	21-Jan-27	$844,533.44	$682,383.02	100%	80.8%
	Geotextile & Bedding	206	01-Jun-26	17-Aug-26	12-Jan-26 A	20-Mar-27	1,432,939.9	$465,705.48	100%	32.5%
	Installation of geotextile lining and coarse sand bedding	206	01-Jun-26	17-Aug-26	12-Jan-26 A	20-Mar-27	1,432,939.9	$465,705.48	100%	32.5%
	Concrete Structures	45	17-Aug-26	10-Oct-26	07-Apr-26 A	26-Nov-26 A	1,031,983.5	1,031,983.5	97.84%	100%
	Construction of pond slab, walls, vertical structures	45	17-Aug-26	10-Oct-26	07-Apr-26 A	26-Nov-26 A	1,031,983.5	1,031,983.5	97.84%	100%
	Energy Dissipation & Siphon Structures	24	26-Sep-26	14-Nov-26	18-Nov-25 A	01-Dec-26 A	$237,986.24	$237,986.24	9.6%	100%
	Siphon pipes, energy dissipators, and associated civil works	24	26-Sep-26	14-Nov-26	18-Nov-25 A	01-Dec-26 A	$237,986.24	$237,986.24	9.6%	100%
	Road Crossing Zone 3	263	22-Jan-26	13-Oct-26	01-Apr-26 A	30-Jun-27	$827,989.78	$300,711.19	98.5%	36.32%
	uPVC Road Crossing Pipes	167	22-Jan-26	22-Jun-26	01-Apr-26 A	24-Feb-27	$601,422.38	$300,711.19	100%	50%
	Installation of uPVC pipes of various diameters crossing roadways	167	22-Jan-26	22-Jun-26	01-Apr-26 A	24-Feb-27	$601,422.38	$300,711.19	100%	50%
	GRP Road Crossing Pipes	96	22-Jun-26	13-Oct-26	24-Feb-27	30-Jun-27	$226,567.41	$0.00	94.5%	0%
	Installation of GRP pipes (800mm–1000mm dia) for road crossings	96	22-Jun-26	13-Oct-26	24-Feb-27	30-Jun-27	$226,567.41	$0.00	94.5%	0%
	Zone 2	590	19-Oct-25	08-Dec-26	15-Oct-25 A	02-Aug-27	31,359,284.0	25,280,286.6	99.09%	80.61%
	Sewerage Network Zone 2	332	19-Oct-25	04-Mar-26	04-Jan-26 A	08-Dec-26	2,599,280.7	1,718,764.2	100%	66.12%
	Pipework: Supply, Installation, and Testing	320	19-Oct-25	03-Feb-26	04-Jan-26 A	25-Nov-26	$739,449.88	$637,141.62	100%	86.16%
	UPVC Pipes Installation (150mm–315mm)	212	19-Oct-25	26-Jan-26	04-Jan-26 A	15-Apr-26 A	$365,941.45	$365,941.45	100%	100%
	GRP Pipes Installation (400mm–700mm)	207	19-Oct-25	03-Feb-26	05-Jan-26 A	06-Apr-26 A	$165,141.29	$165,141.29	100%	100%
	HDPE Pressure Pipes Installation (250mm–630mm)	307	19-Oct-25	03-Feb-26	11-Jan-26 A	25-Nov-26	$208,367.13	$106,058.87	100%	50.9%
	Fittings and Valves	27	21-Dec-25	20-Jan-26	26-Oct-26	26-Nov-26	$61,422.41	$0.00	100%	0%
	Valve & Flow Meter Chambers	148	19-Oct-25	10-Feb-26	01-Jul-26 A	08-Dec-26	$99,848.78	$36,441.43	100%	36.5%
	Valve Chambers Construction	127	19-Oct-25	04-Jan-26	01-Jul-26 A	17-Nov-26	$13,788.12	$5,584.19	100%	40.5%
	Water Drain Chambers Construction	69	19-Oct-25	23-Jan-26	28-Jul-26 A	27-Nov-26	$44,788.55	$18,139.36	100%	40.5%
	Discharge Chambers Construction	76	19-Oct-25	05-Feb-26	14-Jul-26 A	03-Dec-26	$31,287.23	$11,419.84	100%	36.5%
	Flow Meter Chambers Construction	81	19-Oct-25	10-Feb-26	19-Aug-26 A	08-Dec-26	$9,984.88	$1,298.03	100%	13%
	Manholes	266	19-Oct-25	04-Mar-26	01-Feb-26 A	14-Nov-26	1,698,559.6	1,045,181.1	100%	61.53%
	1200mm GRP Manholes with Backdrop	260	19-Oct-25	19-Jan-26	01-Feb-26 A	08-Nov-26	$845,258.26	$527,441.15	100%	62.4%
	1500mm GRP Manholes (Standard & Backdrop)	263	19-Oct-25	09-Feb-26	12-Feb-26 A	11-Nov-26	$800,529.72	$484,720.75	100%	60.55%
	1800mm GRP Manholes (Standard & Backdrop)	265	19-Oct-25	26-Feb-26	14-Feb-26 A	13-Nov-26	$39,936.34	$24,920.27	100%	62.4%
	2000mm GRP Manholes (Standard & Backdrop)	266	19-Oct-25	04-Mar-26	14-Feb-26 A	14-Nov-26	$12,647.05	$7,910.73	100%	62.55%
	Rainwater Drainage Network Zone 2	324	19-Oct-25	18-Jan-26	15-Oct-25 A	10-Nov-26	11,222,278.1	8,656,753.3	100%	77.14%
	Pipe Laying Works	97	19-Oct-25	18-Jan-26	26-Nov-25 A	07-Oct-26	1,182,605.2	1,149,278.9	100%	97.18%
	Supply & Installation of uPVC Pipes (250–300mm dia)	61	19-Oct-25	13-Dec-25	26-Nov-25 A	04-Oct-26	$753,889.26	$725,618.41	100%	96.25%
	Supply & Installation of GRP Pipes (350–800mm dia)	97	19-Oct-25	18-Jan-26	27-Nov-25 A	16-Aug-26 A	$344,458.82	$344,458.82	100%	100%
	uPVC Connection Pipes (150mm dia)	92	19-Oct-25	05-Jan-26	26-Nov-25 A	07-Oct-26	$84,257.13	$79,201.71	100%	94%
	Precast Concrete Box Culverts	154	19-Oct-25	18-Jan-26	01-Apr-26 A	09-Nov-26	2,313,473.6	1,037,200.9	100%	44.83%
	Box Culverts (500x500mm to 3500x800mm)	154	19-Oct-25	18-Jan-26	01-Apr-26 A	09-Nov-26	2,120,070.2	$866,578.70	100%	40.88%
	Tube Culverts at Road Intersections	22	27-Nov-25	18-Jan-26	09-Apr-26 A	10-Oct-26	$178,976.28	$167,700.78	100%	93.7%
	Box Culverts at Road Intersections	138	30-Nov-25	18-Jan-26	22-Apr-26 A	03-Nov-26	$14,427.10	$2,921.49	100%	20.25%
	Manholes	193	13-Dec-25	18-Jan-26	01-Jan-26 A	10-Nov-26	1,560,076.2	$695,055.97	100%	44.55%
	Circular GRP Manholes (1200–1800mm dia)	178	13-Dec-25	18-Jan-26	01-Jan-26 A	22-Oct-26	$457,417.51	$345,578.93	100%	75.55%
	Concrete Manholes for 1500x1500 Box Pipes	117	13-Dec-25	11-Jan-26	10-Feb-26 A	25-Oct-26	$709,008.59	$341,210.38	100%	48.13%
	Concrete Manholes for 1000x1000 Box Pipes	130	13-Dec-25	15-Jan-26	02-Mar-26 A	10-Nov-26	$393,650.15	$8,266.65	100%	2.1%
	Chambers and Catch Basins	89	13-Dec-25	18-Jan-26	15-Oct-25 A	25-Jun-26 A	1,215,935.8	1,215,935.8	100%	100%
	Gully Outfalls	85	13-Dec-25	18-Jan-26	15-Oct-25 A	25-Jun-26 A	$358,131.09	$358,131.09	100%	100%
	Rainwater Catch Basins	88	13-Dec-25	11-Jan-26	29-Dec-25 A	25-Jun-26 A	$521,605.08	$521,605.08	100%	100%
	Precast Chambers for Absorption Pits	74	13-Dec-25	18-Jan-26	30-Dec-25 A	06-Apr-26 A	$336,199.68	$336,199.68	100%	100%
	Gully Outfalls to Swales	196	24-Dec-25	18-Jan-26	01-Feb-26 A	25-Oct-26	$353,796.54	$264,993.61	100%	74.9%
	Gully Outfalls to Swales	187	24-Dec-25	18-Jan-26	01-Feb-26 A	14-Oct-26	$283,037.24	$241,289.24	100%	85.25%
	Riprap Works & Protection	128	24-Dec-25	14-Jan-26	01-Feb-26 A	25-Oct-26	$70,759.31	$23,704.37	100%	33.5%
	Backfilling & Bedding	148	03-Nov-25	06-Jan-26	01-Dec-25 A	12-Oct-26	4,596,390.6	4,294,288.0	100%	93.43%
	Backfilling Materials (Type A– 201–700mm Pipes)	148	03-Nov-25	06-Jan-26	05-Jan-26 A	22-Aug-26 A	3,066,757.0	3,066,757.0	100%	100%
	Gravel Bedding & Filter Cloth for uPVC Drain Pipes	41	27-Nov-25	06-Jan-26	01-Dec-25 A	12-Oct-26	1,529,633.5	1,227,530.9	100%	80.25%
	Potable Water Network Zone 2	319	19-Oct-25	13-Jan-26	23-Dec-25 A	25-Nov-26	3,369,461.9	2,947,703.0	100%	87.48%

2025: Jun | Jul | Aug | Sep | Oct

© Oracle Corporation

Development of Phase One – Part Two – Third Industrial

2026 | 2027 | 2028

Nov | Dec | Jan | Feb | Mar | Apr | May | Jun | Jul | Aug | Sep | Oct | Nov | Dec | Jan | Feb | Mar | Apr | May | Jun | Jul | Aug | Sep | Oct | Nov | Dec | Jan

05-Jan-27, General Site Preparation
21-Jan-27, Backfilling Works
20-Mar-27, Geotextile & Bedding
20-Mar-27, Installation of geotextile lining and coarse sand bedding
26-Nov-26 A, Concrete Structures
26-Nov-26 A, Construction of pond slab, walls, vertical structures
01-Dec-26 A, Energy Dissipation & Siphon Structures
01-Dec-26 A, Siphon pipes, energy dissipators, and associated civil works
30-Jun-27, Road Crossing Zone 3
24-Feb-27, uPVC Road Crossing Pipes
24-Feb-27, Installation of uPVC pipes of various diameters crossing roadways
30-Jun-27, GRP Road Crossing Pipes
30-Jun-27, Installation of GRP pipes (800mm–1000mm dia) for road crossings
02-Aug-27, Zone 2
08-Dec-26, Sewerage Network Zone 2
25-Nov-26, Pipework: Supply, Installation, and Testing
15-Apr-26 A, UPVC Pipes Installation (150mm–315mm)
06-Apr-26 A, GRP Pipes Installation (400mm–700mm)
25-Nov-26, HDPE Pressure Pipes Installation (250mm–630mm)
26-Nov-26, Fittings and Valves
08-Dec-26, Valve & Flow Meter Chambers
17-Nov-26, Valve Chambers Construction
27-Nov-26, Water Drain Chambers Construction
03-Dec-26, Discharge Chambers Construction
08-Dec-26, Flow Meter Chambers Construction
14-Nov-26, Manholes
08-Nov-26, 1200mm GRP Manholes with Backdrop
11-Nov-26, 1500mm GRP Manholes (Standard & Backdrop)
13-Nov-26, 1800mm GRP Manholes (Standard & Backdrop)
14-Nov-26, 2000mm GRP Manholes (Standard & Backdrop)
10-Nov-26, Rainwater Drainage Network Zone 2
07-Oct-26, Pipe Laying Works
04-Oct-26, Supply & Installation of uPVC Pipes (250–300mm dia)
16-Aug-26 A, Supply & Installation of GRP Pipes (350–800mm dia)
07-Oct-26, uPVC Connection Pipes (150mm dia)
09-Nov-26, Precast Concrete Box Culverts
09-Nov-26, Box Culverts (500x500mm to 3500x800mm)
10-Oct-26, Tube Culverts at Road Intersections
03-Nov-26, Box Culverts at Road Intersections
10-Nov-26, Manholes
22-Oct-26, Circular GRP Manholes (1200–1800mm dia)
25-Oct-26, Concrete Manholes for 1500x1500 Box Pipes
10-Nov-26, Concrete Manholes for 1000x1000 Box Pipes
25-Jun-26 A, Chambers and Catch Basins
25-Jun-26 A, Gully Outfalls
25-Jun-26 A, Rainwater Catch Basins
06-Apr-26 A, Precast Chambers for Absorption Pits
25-Oct-26, Gully Outfalls to Swales
14-Oct-26, Gully Outfalls to Swales
25-Oct-26, Riprap Works & Protection
12-Oct-26, Backfilling & Bedding
22-Aug-26 A, Backfilling Materials (Type A – 201–700mm Pipes)
12-Oct-26, Gravel Bedding & Filter Cloth for uPVC Drain Pipes
25-Nov-26, Potable Water Network Zone 2

Actual Level of Effort | Actual Work | Remaining Work | Critical Remaining Work | Milestone | summary

TASK filter: All Activities

© Oracle Corporation

Development of Phase One – Part Two – Third Industrial

Activity ID	Activity Name	Original Duration	BL Project Start	BL Project Finish	Start	Finish	Budgeted Total Cost	Earned Value Cost	Schedule % Complete	Performance % Complete
	Pipe Installation Works	73	19-Oct-25	14-Dec-25	23-Dec-25 A	04-Oct-26	2,004,732.2	1,944,590.2	100%	97%
	Valve Installation & Chambers	117	09-Nov-25	31-Dec-25	01-Apr-26 A	17-Oct-26	$632,606.85	$485,146.19	100%	76.69%
	Flow Meter Installation	74	23-Nov-25	13-Jan-26	30-Aug-26 A	25-Nov-26	$123,072.32	$38,767.78	100%	31.5%
	Washout & Air Valve Chambers	114	09-Nov-25	07-Jan-26	01-May-26 A	12-Oct-26	$609,050.48	$479,198.77	100%	78.68%
	Irrigation Network Zone 2	309	19-Oct-25	18-Jan-26	20-Nov-25 A	08-Nov-26	1,665,247.6	1,525,022.0	100%	91.58%
	Excavation, Pipe Laying & Backfilling	122	19-Oct-25	14-Dec-25	20-Nov-25 A	05-Oct-26	1,092,569.0	1,010,626.3	100%	92.5%
	Valves and Appurtenances	69	07-Dec-25	29-Dec-25	05-Feb-26 A	07-Oct-26	$127,197.68	$104,034.60	100%	81.79%
	Valve Rooms	64	21-Dec-25	18-Jan-26	30-Jan-26 A	04-Oct-26	$120,296.07	$119,093.11	100%	99%
	Washout Chambers	29	21-Dec-25	18-Jan-26	18-Apr-26 A	05-Oct-26	$140,613.57	$134,989.03	100%	96%
	Air Valve Chambers	20	25-Dec-25	18-Jan-26	23-Mar-26 A	28-Jul-26 A	$94,896.71	$94,896.71	100%	100%
	Flow Meter Chambers	145	21-Dec-25	18-Jan-26	01-Apr-26 A	08-Nov-26	$89,674.62	$61,382.28	100%	68.45%
	Rainwater Collection Ponds Zone 2	256	19-Jan-26	08-Dec-26	27-Oct-25 A	01-Apr-27	10,847,036.1	10,432,043.9	97.59%	96.17%
	Excavation for Rainwater Drainage Pond	54	19-Jan-26	14-Mar-26	01-May-26 A	09-Jan-27	$112,754.77	$98,322.16	100%	87.2%
	Deep excavation, backfill, disposal for pond formation	54	19-Jan-26	14-Mar-26	01-May-26 A	09-Jan-27	$112,754.77	$98,322.16	100%	87.2%
	General Site Preparation	61	22-Jan-26	08-Jun-26	27-Oct-25 A	08-Sep-26 A	9,720,726.1	9,720,726.1	100%	100%
	Backfilling Works	165	08-Jun-26	23-Aug-26	17-Nov-25 A	21-Jan-27	$241,295.27	$184,590.88	100%	76.5%
	Geotextile & Bedding	213	25-Jun-26	10-Sep-26	04-Jan-26 A	23-Mar-27	$409,411.41	$98,258.74	100%	24%
	Installation of geotextile lining and coarse sand bedding	213	25-Jun-26	10-Sep-26	04-Jan-26 A	23-Mar-27	$409,411.41	$98,258.74	100%	24%
	Concrete Structures	73	10-Sep-26	03-Nov-26	02-Mar-26 A	01-Apr-27	$294,852.45	$262,149.99	34.58%	88.91%
	Construction of pond slab, walls, vertical structures	73	10-Sep-26	03-Nov-26	02-Mar-26 A	01-Apr-27	$294,852.45	$262,149.99	34.58%	88.91%
	Energy Dissipation & Siphon Structures	42	20-Oct-26	08-Dec-26	09-Dec-25 A	15-Jan-26 A	$67,996.07	$67,996.07	0%	100%
	Siphon pipes, energy dissipators, and associated civil works	42	20-Oct-26	08-Dec-26	09-Dec-25 A	15-Jan-26 A	$67,996.07	$67,996.07	0%	100%
	Road Crossing Zone 2	164	22-Jan-26	13-Oct-26	31-Dec-26	02-Aug-27	1,655,979.5	$0.00	98.5%	0%
	uPVC Road Crossing Pipes	68	22-Jan-26	22-Jun-26	31-Dec-26	07-Apr-27	1,202,844.7	$0.00	100%	0%
	Installation of uPVC pipes of various diameters crossing roadways	68	22-Jan-26	22-Jun-26	31-Dec-26	07-Apr-27	1,202,844.7	$0.00	100%	0%
	GRP Road Crossing Pipes	96	22-Jun-26	13-Oct-26	08-Apr-27	02-Aug-27	$453,134.81	$0.00	94.5%	0%
	Installation of GRP pipes (800mm–1000mm dia) for road crossings	96	22-Jun-26	13-Oct-26	08-Apr-27	02-Aug-27	$453,134.81	$0.00	94.5%	0%
	Zone 1	691	13-Oct-25	08-Feb-27	22-Jul-25 A	19-Oct-27	33,088,596.0	18,765,955.7	89.33%	77.3%
	Sewerage Network Zone 1	449	13-Oct-25	28-Dec-26	03-Nov-25 A	08-Mar-27	8,652,451.5	2,582,075.8	49.3%	29.84%
	Pipework: Supply, Installation, and Testing	120	19-Oct-25	03-Feb-26	03-Nov-25 A	10-Oct-26	$739,449.88	$727,989.69	100%	98.45%
	UPVC Pipes Installation (150mm–315mm)	114	19-Oct-25	26-Jan-26	03-Nov-25 A	18-Mar-26 A	$365,941.45	$365,941.45	100%	100%
	GRP Pipes Installation (400mm–700mm)	110	19-Oct-25	03-Feb-26	17-Nov-25 A	28-Feb-26 A	$165,141.29	$165,141.29	100%	100%
	HDPE Pressure Pipes Installation (250mm–630mm)	114	19-Oct-25	03-Feb-26	22-Nov-25 A	10-Oct-26	$208,367.13	$196,906.94	100%	94.5%
	Fittings and Valves	27	21-Dec-25	20-Jan-26	05-Oct-26	05-Nov-26	$61,422.41	$0.00	100%	0%
	Valve & Flow Meter Chambers	153	19-Oct-25	10-Feb-26	01-Jun-26 A	17-Dec-26	$99,848.78	$37,677.75	100%	37.73%
	Valve Chambers Construction	71	19-Oct-25	04-Jan-26	01-Jun-26 A	29-Nov-26	$13,788.12	$3,447.03	100%	25%
	Water Drain Chambers Construction	133	19-Oct-25	23-Jan-26	11-Jul-26 A	27-Nov-26	$44,788.55	$22,170.33	100%	49.5%
	Discharge Chambers Construction	88	19-Oct-25	05-Feb-26	13-Jul-26 A	15-Dec-26	$31,287.23	$7,821.81	100%	25%
	Flow Meter Chambers Construction	153	19-Oct-25	10-Feb-26	11-Jul-26 A	17-Dec-26	$9,984.88	$4,238.58	100%	42.45%
	Manholes	288	19-Oct-25	08-Jan-26	31-Dec-25 A	24-Oct-26	1,698,559.6	1,136,398.7	100%	66.9%
	1200mm GRP Manholes with Backdrop	288	19-Oct-25	24-Dec-25	01-Jan-26 A	24-Oct-26	$845,258.26	$565,477.77	100%	66.9%
	1500mm GRP Manholes (Standard & Backdrop)	288	19-Oct-25	29-Dec-25	03-Jan-26 A	24-Oct-26	$800,529.72	$535,554.38	100%	66.9%
	1800mm GRP Manholes (Standard & Backdrop)	288	19-Oct-25	30-Dec-25	05-Jan-26 A	24-Oct-26	$39,936.34	$26,717.41	100%	66.9%
	2000mm GRP Manholes (Standard & Backdrop)	288	19-Oct-25	08-Jan-26	06-Jan-26 A	24-Oct-26	$12,647.05	$8,460.87	100%	66.9%
	Pumping Stations	241	13-Oct-25	28-Dec-26	01-Jan-26 A	08-Mar-27	6,053,170.7	$680,009.70	27.53%	11.23%
	Perimeter Walls & Gates	65	13-Oct-25	11-Dec-25	01-Apr-26 A	07-Oct-26	$391,592.83	$372,775.20	100%	95.19%
	Sewage Pumps and MCC System	44	08-Nov-26	28-Dec-26	29-Oct-26	20-Dec-26	1,650,424.4	$0.00	0%	0%
	Odor Control System	25	31-Aug-26	25-Oct-26	30-Nov-26	29-Dec-26	$276,510.51	$0.00	56.96%	0%
	In-Line Booster Stations	63	28-Sep-26	10-Dec-26	12-Dec-26	08-Mar-27	1,968,220.0	$0.00	5.08%	0%
	Engine/Motor Control Center Buildings	8	06-Nov-25	08-Dec-25	03-Oct-26	11-Oct-26	$45,941.19	$0.00	100%	0%
	Valves and Fittings (General Supply & Installation)	5	18-Dec-25	23-Dec-25	29-Oct-26	04-Nov-26	$23,484.26	$0.00	100%	0%
	Tank with Canopy	13	22-Oct-26	07-Nov-26	05-Jan-27	20-Jan-27	$748,883.49	$0.00	0%	0%
	Pump Well and Valve Chambers	62	19-Nov-25	29-Jan-26	04-Oct-26	14-Dec-26	$442,703.31	$0.00	100%	0%
	Odor Control System Base/Plinth	6	25-Dec-25	31-Dec-25	25-Oct-26	31-Oct-26	$16,590.51	$0.00	100%	0%


2025: Jun | Jul | Aug | Sep | Oct

Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary

TASK filter: All Activities

© Oracle Corporation

Development of Phase One – Part Two – Third Industrial

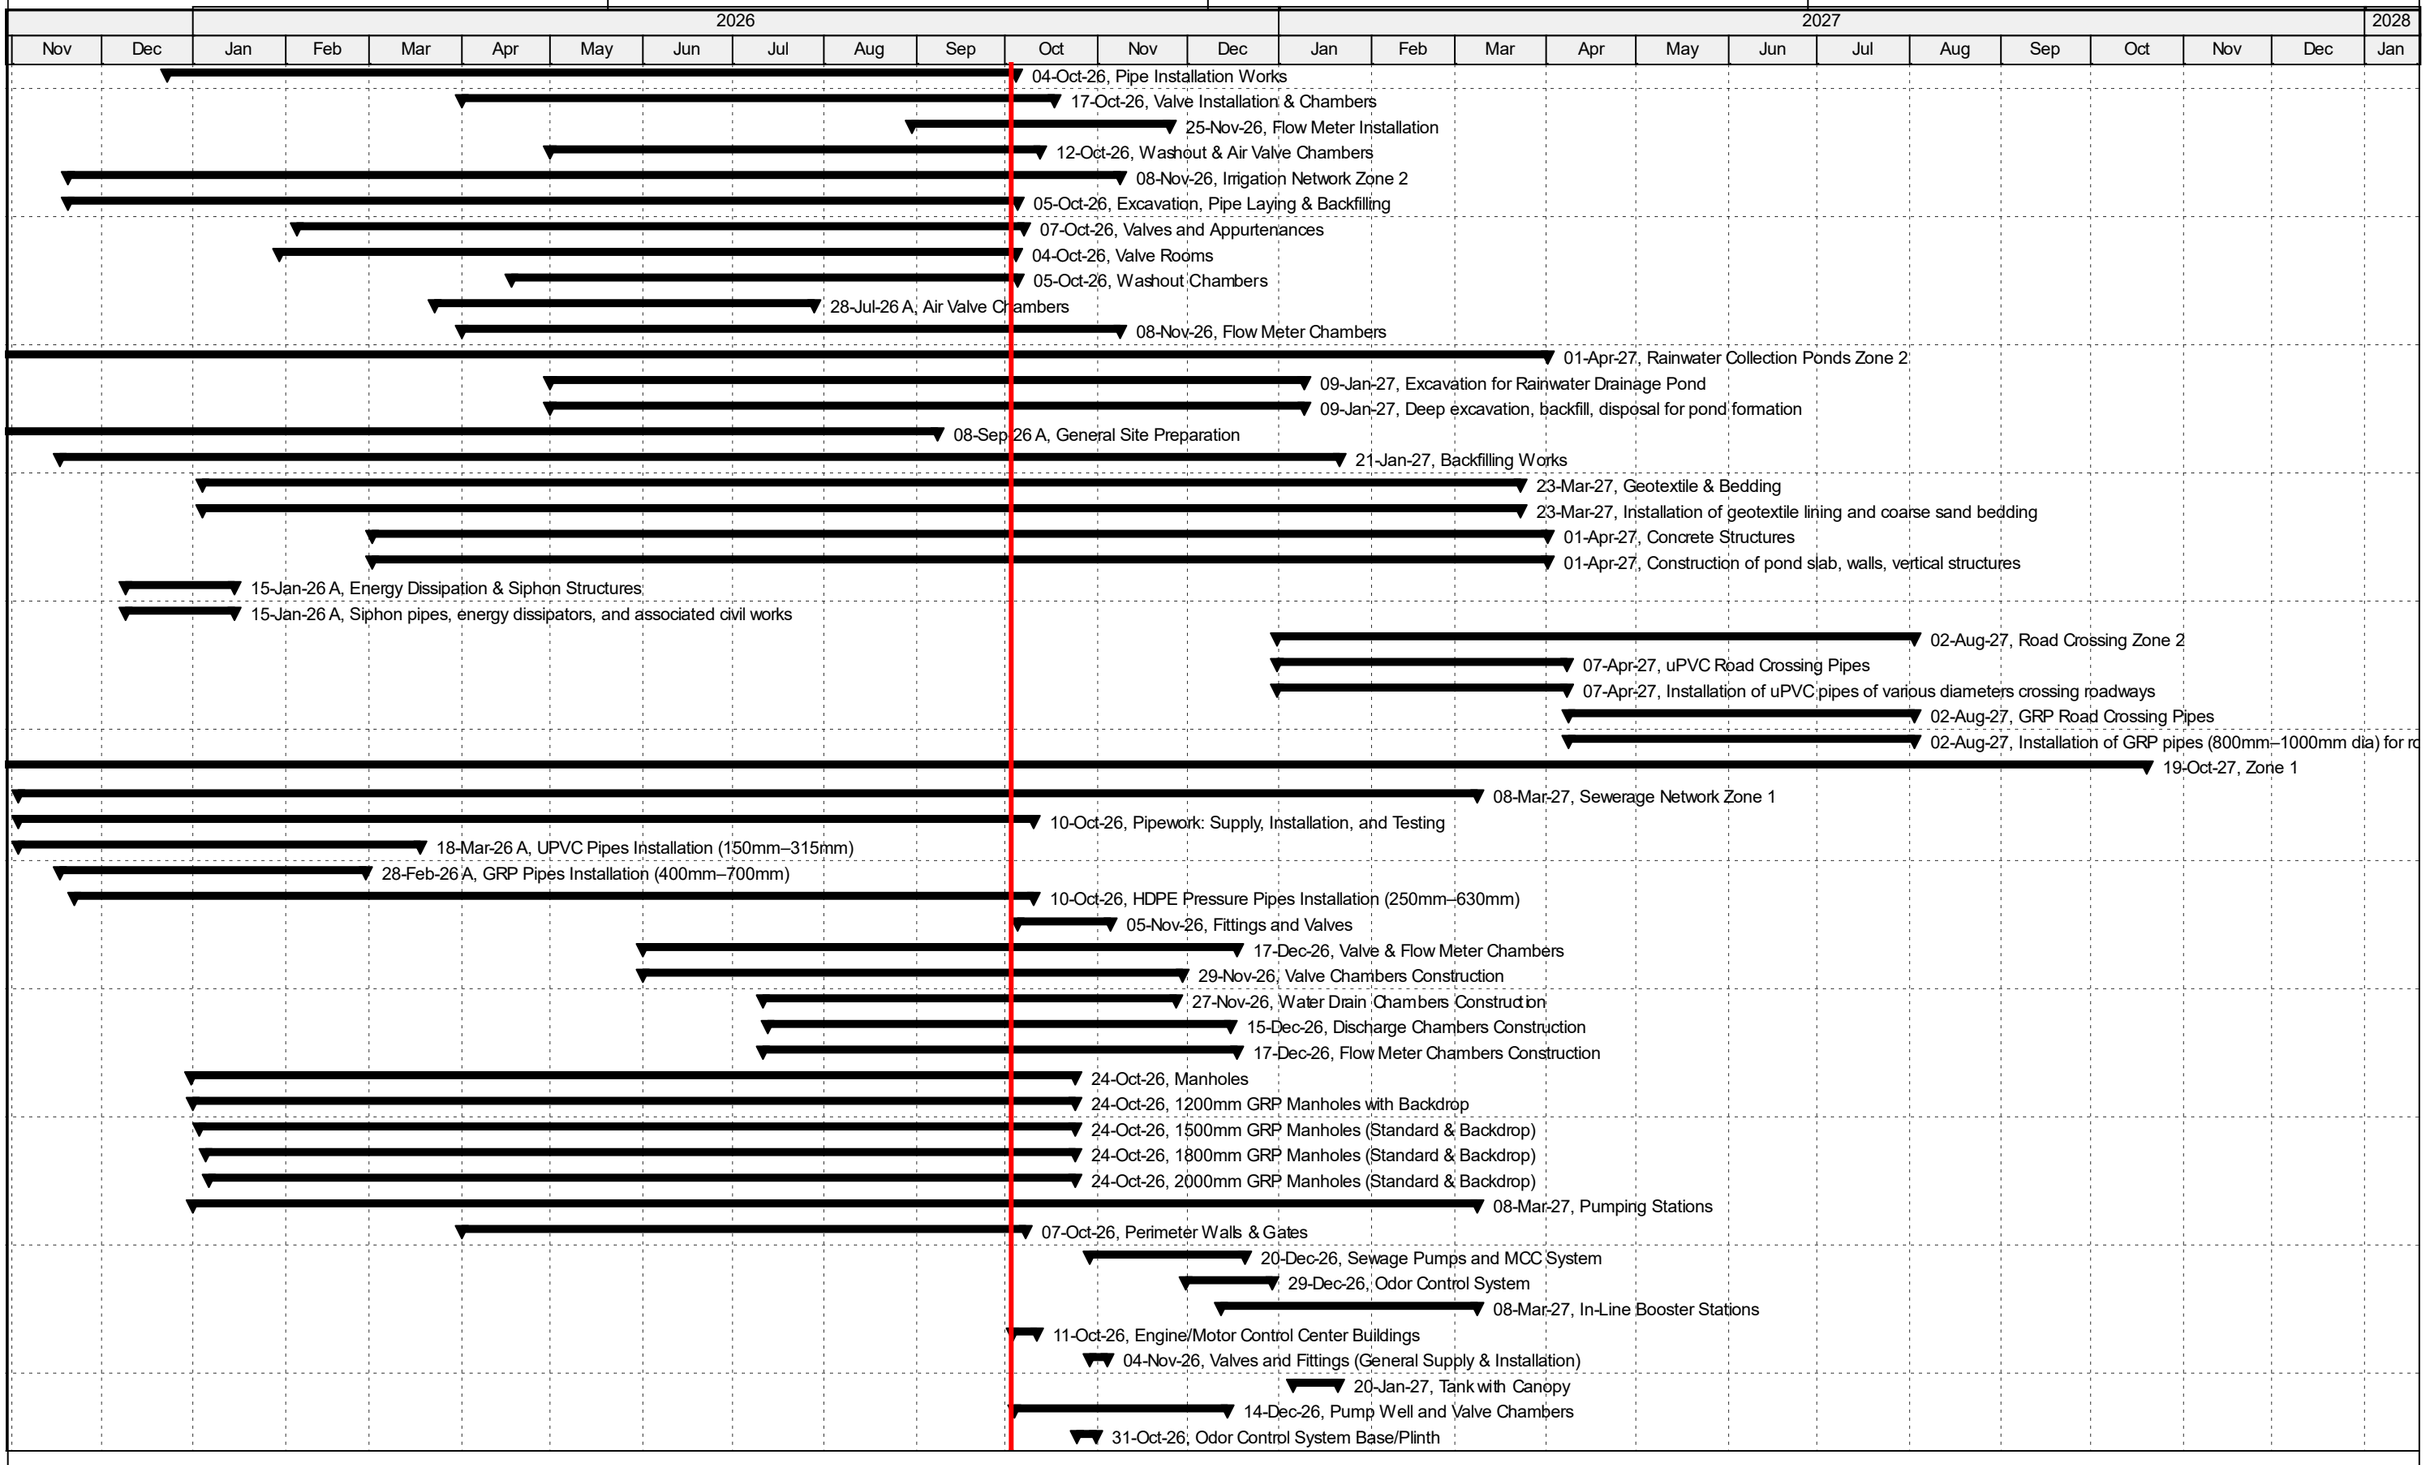

Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary

TASK filter: All Activities

© Oracle Corporation

Development of Phase One – Part Two – Third Industrial

Activity ID	Activity Name	Original Duration	BL Project Start	BL Project Finish	Start	Finish	Budgeted Total Cost	Earned Value Cost	Schedule % Complete	Performance % Complete
	Lighting Works	13	13-Dec-25	27-Dec-25	01-Jan-26 A	29-Oct-26	$384,043.12	$307,234.50	100%	80%
	Duct Works	7	04-Dec-25	11-Dec-25	19-Oct-26	26-Oct-26	$15,220.07	$0.00	100%	0%
	Grounding Works	3	13-Dec-25	15-Dec-25	27-Oct-26	29-Oct-26	$7,603.32	$0.00	100%	0%
	Landscaping / Interlocking Tiles	21	06-Dec-25	29-Dec-25	05-Oct-26	28-Oct-26	$61,674.68	$0.00	100%	0%
	Pumping Station Internal Drainage Network	7	01-Dec-25	08-Dec-25	03-Oct-26	10-Oct-26	$20,278.98	$0.00	100%	0%
	Rainwater Drainage Network Zone 1	326	19-Oct-25	18-Jan-26	01-Oct-25 A	02-Nov-26	1,222,278.1	9,286,386.7	100%	82.75%
	Pipe Laying Works	101	19-Oct-25	18-Jan-26	01-Oct-25 A	11-Oct-26	1,182,605.2	1,121,322.9	100%	94.82%
	Supply & Installation of uPVC Pipes (250–300mm dia)	77	19-Oct-25	13-Dec-25	01-Oct-25 A	06-Oct-26	$753,889.26	$701,117.01	100%	93%
	Supply & Installation of GRP Pipes (350–800mm dia)	71	19-Oct-25	18-Jan-26	15-Dec-25 A	16-Aug-26 A	$344,458.82	$344,458.82	100%	100%
	uPVC Connection Pipes (150mm dia)	46	19-Oct-25	05-Jan-26	15-Dec-25 A	11-Oct-26	$84,257.13	$75,747.16	100%	89.9%
	Precast Concrete Box Culverts	147	19-Oct-25	06-Jan-26	01-Apr-26 A	01-Nov-26	2,313,473.6	1,533,939.8	100%	66.3%
	Box Culverts (500x500mm to 3500x800mm)	142	19-Oct-25	06-Jan-26	01-Apr-26 A	27-Oct-26	2,120,070.2	1,436,347.5	100%	67.75%
	Tube Culverts at Road Intersections	135	10-Nov-25	04-Jan-26	01-Apr-26 A	21-Oct-26	$178,976.28	$95,304.87	100%	53.25%
	Box Culverts at Road Intersections	142	12-Nov-25	01-Jan-26	13-Apr-26 A	01-Nov-26	$14,427.10	$2,287.42	100%	15.86%
	Manholes	240	25-Nov-25	18-Jan-26	01-Jan-26 A	02-Nov-26	1,560,076.2	1,049,796.6	100%	67.29%
	Circular GRP Manholes (1200–1800mm dia)	47	25-Nov-25	18-Jan-26	01-Jan-26 A	24-Oct-26	$457,417.51	$332,885.60	100%	72.78%
	Concrete Manholes for 1500x1500 Box Pipes	234	25-Nov-25	17-Jan-26	01-Jan-26 A	26-Oct-26	$709,008.59	$501,978.08	100%	70.8%
	Concrete Manholes for 1000x1000 Box Pipes	202	25-Nov-25	12-Jan-26	01-Jan-26 A	02-Nov-26	$393,650.15	$214,932.98	100%	54.6%
	Chambers and Catch Basins	99	25-Nov-25	18-Jan-26	28-Dec-25 A	10-Oct-26	1,215,935.8	1,213,849.4	100%	99.83%
	Gully Outfalls	42	25-Nov-25	12-Jan-26	31-Dec-25 A	28-Feb-26 A	$358,131.09	$358,131.09	100%	100%
	Rainwater Catch Basins	77	13-Dec-25	14-Jan-26	28-Dec-25 A	10-Oct-26	$521,605.08	$519,518.66	100%	99.6%
	Precast Chambers for Absorption Pits	84	13-Dec-25	18-Jan-26	01-Jan-26 A	24-Mar-26 A	$336,199.68	$336,199.68	100%	100%
	Gully Outfalls to Swales	75	20-Dec-25	18-Jan-26	31-Dec-25 A	13-Oct-26	$353,796.54	$314,949.68	100%	89.02%
	Gully Outfalls to Swales	72	20-Dec-25	07-Jan-26	31-Dec-25 A	11-Oct-26	$283,037.24	$262,800.07	100%	92.85%
	Riprap Works & Protection	29	03-Jan-26	18-Jan-26	01-Feb-26 A	13-Oct-26	$70,759.31	$52,149.61	100%	73.7%
	Backfilling & Bedding	203	02-Nov-25	18-Jan-26	01-Jan-26 A	19-Oct-26	4,596,390.6	4,052,528.1	100%	88.17%
	Backfilling Materials (Type A– 201–700mm Pipes)	197	10-Nov-25	18-Jan-26	01-Jan-26 A	13-Oct-26	3,066,757.0	2,721,746.9	100%	88.75%
	Gravel Bedding & Filter Cloth for uPVC Drain Pipes	186	02-Nov-25	18-Jan-26	03-Feb-26 A	19-Oct-26	1,529,633.5	1,330,781.2	100%	87%
	Potable Water Network Zone 1	366	19-Oct-25	17-Jan-26	09-Sep-25 A	29-Nov-26	3,369,461.9	2,994,625.6	100%	88.88%
	Pipe Installation Works	63	19-Oct-25	14-Dec-25	09-Sep-25 A	04-Oct-26	2,004,732.2	1,918,528.7	100%	95.7%
	Valve Installation & Chambers	177	09-Nov-25	27-Dec-25	01-Feb-26 A	06-Oct-26	$632,606.85	$543,092.98	100%	85.85%
	Flow Meter Installation	154	09-Nov-25	17-Jan-26	01-May-26 A	29-Nov-26	$123,072.32	$45,044.47	100%	36.6%
	Washout & Air Valve Chambers	114	09-Nov-25	06-Jan-26	01-May-26 A	13-Oct-26	$609,050.48	$487,959.41	100%	80.12%
	Irrigation Network Zone 1	330	19-Oct-25	18-Jan-26	04-Nov-25 A	09-Nov-26	1,665,247.6	1,566,078.6	100%	94.04%
	Excavation, Pipe Laying & Backfilling	124	19-Oct-25	14-Dec-25	04-Nov-25 A	03-Oct-26	1,092,569.0	1,079,458.1	100%	98.8%
	Valves and Appurtenances	79	07-Dec-25	29-Dec-25	01-Feb-26 A	06-Oct-26	$127,197.68	$116,487.63	100%	91.58%
	Valve Rooms	68	25-Dec-25	18-Jan-26	01-Feb-26 A	07-Oct-26	$120,296.07	$99,148.02	100%	82.42%
	Washout Chambers	52	22-Dec-25	18-Jan-26	01-May-26 A	03-Oct-26	$140,613.57	$139,769.89	100%	99.4%
	Air Valve Chambers	22	22-Dec-25	13-Jan-26	22-Mar-26 A	27-Jul-26 A	$94,896.71	$94,896.71	100%	100%
	Flow Meter Chambers	149	22-Dec-25	18-Jan-26	13-Apr-26 A	09-Nov-26	$89,674.62	$36,318.22	100%	40.5%
	Rainwater Collection Ponds Zone 1	280	19-Jan-26	08-Feb-27	22-Jul-25 A	06-Apr-27	36,523,177.3	32,336,788.8	95.14%	88.54%
	Excavation for Rainwater Drainage Pond	221	19-Jan-26	14-Mar-26	22-Jul-25 A	09-Jan-27	$169,132.15	$147,144.97	100%	87%
	Deep excavation, backfill, disposal for pond formation	221	19-Jan-26	14-Mar-26	22-Jul-25 A	09-Jan-27	$169,132.15	$147,144.97	100%	87%
	General Site Preparation	94	16-Feb-26	20-Aug-26	22-Jul-25 A	16-Jan-27	33,469,057.7	31,108,061.7	100%	92.95%
	Backfilling Works	141	27-Jul-26	12-Oct-26	03-Sep-25 A	28-Jan-27	$361,942.90	$271,457.18	80.75%	75%
	Geotextile & Bedding	224	13-Aug-26	31-Oct-26	07-Jan-26 A	09-Mar-27	$614,117.12	$264,377.42	63.86%	43.05%
	Installation of geotextile lining and coarse sand bedding	224	13-Aug-26	31-Oct-26	07-Jan-26 A	09-Mar-27	$614,117.12	$264,377.42	63.86%	43.05%
	Concrete Structures	45	22-Aug-26	14-Oct-26	01-Mar-26 A	25-Apr-26 A	$442,278.68	$442,278.68	95.56%	100%
	Construction of pond slab, walls, vertical structures	45	22-Aug-26	14-Oct-26	01-Mar-26 A	25-Apr-26 A	$442,278.68	$442,278.68	95.56%	100%
	Energy Dissipation & Siphon Structures	42	30-Sep-26	18-Nov-26	01-Oct-25 A	30-Dec-25 A	$101,994.10	$101,994.10	1.4%	100%
	Siphon pipes, energy dissipators, and associated civil works	42	30-Sep-26	18-Nov-26	01-Oct-25 A	30-Dec-25 A	$101,994.10	$101,994.10	1.4%	100%
	Culvert Structures	147	16-Nov-26	08-Feb-27	03-Feb-26 A	06-Apr-27	1,364,654.5	$1,474.78	0%	0.11%
	Access Roads	55	05-Dec-26	08-Feb-27	14-Jan-27	06-Apr-27	1,363,179.7	$0.00	0%	0%
	Construct 3m & 5m wide roads	55	05-Dec-26	08-Feb-27	14-Jan-27	06-Apr-27	1,363,179.7	$0.00	0%	0%


2025: Jun | Jul | Aug | Sep | Oct

Actual Level of Effort · Actual Work · Remaining Work · Critical Remaining Work · Milestone · summary

TASK filter: All Activities

© Oracle Corporation

Development of Phase One – Part Two – Third Industrial

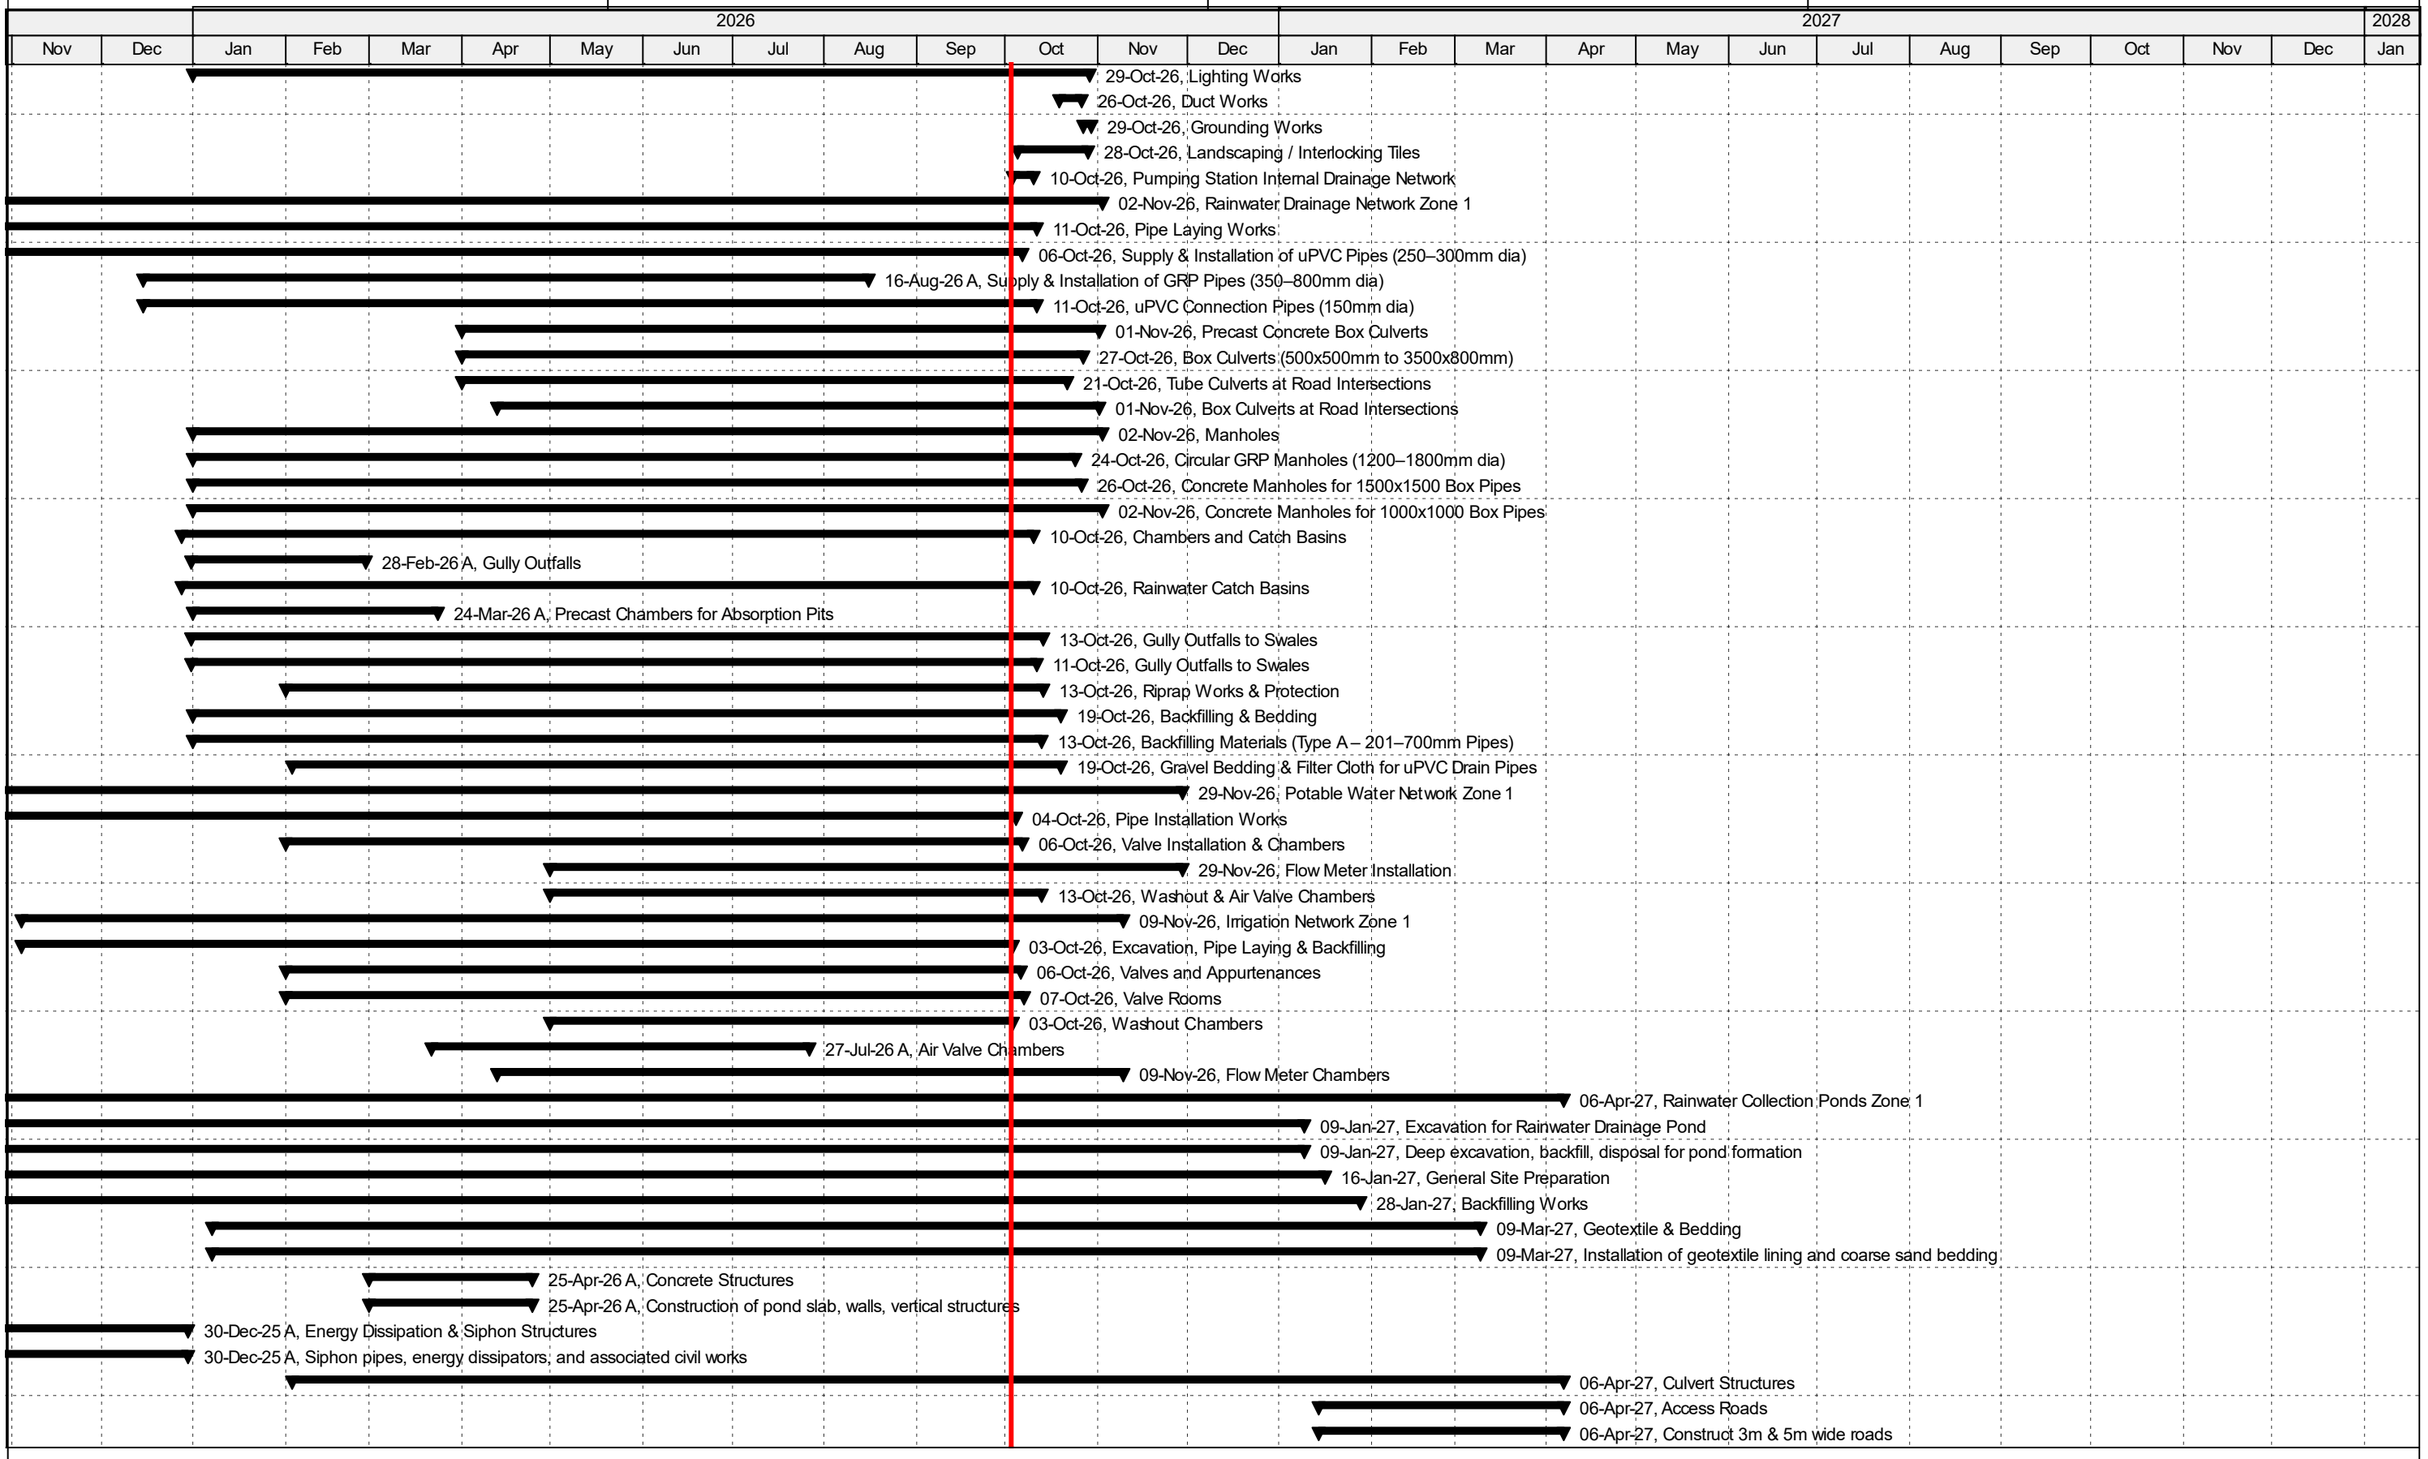


Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary

TASK filter: All Activities

© Oracle Corporation

Development of Phase One – Part Two – Third Industrial

Activity ID	Activity Name	Original Duration	BL Project Start	BL Project Finish	Start	Finish	Budgeted Total Cost	Earned Value Cost	Schedule % Complete	Performance % Complete
	Road Crossing Zone 1	162	22-Jun-26	23-Jan-27	08-Apr-27	19-Oct-27	1,655,979.5	$0.00	65.74%	0%
	uPVC Road Crossing Pipes	110	22-Jun-26	29-Oct-26	08-Apr-27	18-Aug-27	1,202,844.7	$0.00	90.5%	0%
	Installation of uPVC pipes of various diameters crossing roadways	110	22-Jun-26	29-Oct-26	08-Apr-27	18-Aug-27	1,202,844.7	$0.00	90.5%	0%
	GRP Road Crossing Pipes	66	13-Oct-26	23-Jan-27	03-Aug-27	19-Oct-27	$453,134.81	$0.00	0%	0%
	Installation of GRP pipes (800mm–1000mm dia) for road crossings	66	13-Oct-26	23-Jan-27	03-Aug-27	19-Oct-27	$453,134.81	$0.00	0%	0%
	General	864	19-May-25	18-May-27	19-May-25 A	29-Sep-27	15,097,284.2	9,611,809.5	47.93%	63.67%
	General Items	30	19-May-25	17-Jun-25	19-May-25 A	07-Aug-25 A	$162,229.63	$162,229.63	100%	100%
	Site Setup & Facilities	30	19-May-25	17-Jun-25	19-May-25 A	18-Jun-25 A	$53,699.01	$53,699.01	100%	100%
	Project Laboratory	30	19-May-25	17-Jun-25	18-Jun-25 A	07-Aug-25 A	$108,530.62	$108,530.62	100%	100%
	Local Roads	73	29-Aug-26	16-Mar-27	10-Apr-27	08-Jul-27	$83,955.86	$0.00	0.26%	0%
	Bituminous Construction	21	29-Aug-26	27-Dec-26	10-Apr-27	04-May-27	$73,510.98	$0.00	0.3%	0%
	Bituminous Foundation Layer (MC 1)	8	29-Aug-26	12-Dec-26	10-Apr-27	19-Apr-27	$434.07	$0.00	50%	0%
	Bituminous Base Layer (Grade 1 - Class A, 70mm)	5	12-Dec-26	17-Dec-26	19-Apr-27	25-Apr-27	$28,499.23	$0.00	0%	0%
	Bituminous Top Layer (Grade 1 - Class A, 50mm)	8	17-Dec-26	27-Dec-26	25-Apr-27	04-May-27	$44,577.67	$0.00	0%	0%
	Precast Curbs (Type K1-D)	52	27-Dec-26	16-Mar-27	04-May-27	08-Jul-27	$10,444.88	$0.00	0%	0%
	Arterial Roads	154	07-May-26	29-Aug-26	27-Jun-26 A	10-Apr-27	$479,616.37	$49,597.05	100%	10.34%
	Earthworks	2	07-May-26	10-May-26	16-Jan-27	18-Jan-27	$16,092.57	$0.00	100%	0%
	Precast Curbs (Type K1-D)	154	10-May-26	29-Aug-26	27-Jun-26 A	10-Apr-27	$463,523.80	$49,597.05	100%	10.7%
	Communications	234	22-Jun-26	18-May-27	04-Nov-25 A	06-May-27	10,712,645.9	9,399,982.8	56.35%	87.75%
	Ductworks	167	22-Jun-26	14-Feb-27	04-Nov-25 A	18-Apr-27	6,718,317.7	5,623,345.5	89.85%	83.7%
	Concrete-Protected Service Culverts (50mm, 8 Outlets)	148	22-Jun-26	16-Sep-26	04-Nov-25 A	05-Apr-27	5,830,115.7	4,891,467.0	100%	83.9%
	Road Crossing Ducts (Exit 8)	121	16-Sep-26	14-Feb-27	01-Dec-25 A	18-Apr-27	$888,202.07	$731,878.51	23.24%	82.4%
	Manholes (Telecom, 2000x1000x1001mm)	74	14-Feb-27	18-May-27	23-Nov-25 A	06-May-27	3,994,328.1	3,776,637.2	0%	94.55%
	Landscape	171	29-Jul-26	21-Feb-27	28-Feb-27	29-Sep-27	3,658,836.4	$0.00	15.25%	0%
	Supply & Planting of Trees and Shrubs	99	18-Aug-26	13-Dec-26	28-Mar-27	26-Jul-27	1,929,003.8	$0.00	24.43%	0%
	planting of trees, shrubs, and vines	99	18-Aug-26	13-Dec-26	28-Mar-27	26-Jul-27	1,929,003.8	$0.00	24.43%	0%
	Gravel Layer and Bed Preparation	37	29-Jul-26	10-Sep-26	28-Feb-27	20-Apr-27	$86,633.98	$0.00	100%	0%
	Installation of gravel layers and soil beds to support planting and drainage.	37	29-Jul-26	10-Sep-26	28-Feb-27	20-Apr-27	$86,633.98	$0.00	100%	0%
	Landscape Irrigation System	87	05-Nov-26	21-Feb-27	19-Jun-27	29-Sep-27	1,643,198.5	$0.00	0%	0%
	Design, supply, and installation of irrigation lines for arterial road landscape zones.	87	05-Nov-26	21-Feb-27	19-Jun-27	29-Sep-27	1,643,198.5	$0.00	0%	0%
	Testing & Commissioning & Closeout	384	12-Jan-26	18-May-27	14-Jan-26 A	24-Oct-27	23,377,607.6	12,429,541.4	61.84%	53.17%
	Testing & Commissioning	247	12-Jan-26	18-May-27	14-Jan-26 A	11-May-27	23,377,607.6	12,429,541.4	61.84%	53.17%
	Zone 3	229	12-Jan-26	19-Jan-27	20-Jan-26 A	11-May-27	5,908,314.1	2,312,989.8	48.94%	39.15%
	Zone 2	84	14-Jan-26	09-Apr-26	14-Jan-26 A	15-Dec-26	5,782,474.4	4,047,732.1	100%	70%
	Zone 1	207	18-Jan-26	21-Jan-27	18-Jan-26 A	25-Mar-27	8,799,551.3	4,047,732.1	65.71%	46%
	General	21	20-Apr-27	18-May-27	14-Jun-26 A	08-May-27	2,887,267.6	2,021,087.3	0%	70%
	As-Built	221	12-Dec-26	18-May-27	16-Jan-27	24-Oct-27	$0.00	$0.00	0%	0%
	Handover	21	20-Apr-27	18-May-27	09-Jun-27	04-Jul-27	$0.00	$0.00	0%	0%

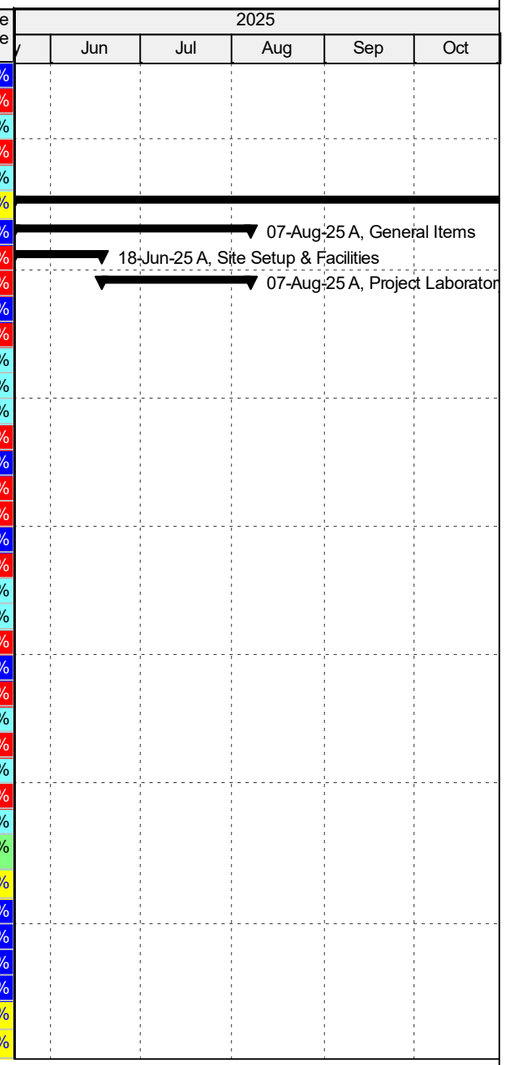

© Oracle Corporation

Development of Phase One – Part Two – Third Industrial



Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary

TASK filter: All Activities

© Oracle Corporation
