
Development of Phase One – Part Two – Third Industrial

Activity ID	Activity Name	Original Duration	BL Project Start	BL Project Finish	Start	Finish	Budgeted Total Cost	Remaining Total Cost	Schedule % Complete
Development of Phase One – Part Two – Third Industrial City in Dammam - 01-C		800	19-May-25	25-Oct-26	19-May-25 A	27-Jul-27	›,296,882.84	$39,925,189.98	99.13%
Milestones		90	16-Jul-25	18-Jan-26	03-Oct-26	31-Dec-26	$0.00	$0.00	0%
MIL-0003	Submission of Report, Work Plan, and Schedule	0		17-Jul-25		03-Oct-26	$0.00	$0.00	100%
MIL-0004	Submission and Approval of Drawings and Specifications	0		16-Jul-25		08-Oct-26*	$0.00	$0.00	100%
MIL-0005	Completion of Water Networks and Tanks	0		18-Jan-26		31-Dec-26*	$0.00	$0.00	100%
MIL-0006	Completion of Rainwater Drainage Works	0		18-Jan-26		31-Dec-26*	$0.00	$0.00	100%
Mobilization		473	19-May-25	13-Aug-25	19-May-25 A	22-Dec-26	$0.00	$0.00	0%
Deliverables		473	19-May-25	13-Aug-25	19-May-25 A	22-Dec-26	$0.00	$0.00	0%
Submittals		463	19-May-25	02-Aug-25	19-May-25 A	10-Dec-26	$0.00	$0.00	0%
S100015	Prepare & Submit Pre-commissioning/ Commissioning Plan/ Startup/ Testing / Handover	60	19-May-25	02-Aug-25	03-Oct-26	10-Dec-26	$0.00	$0.00	100%
S10002	Prepare & Submit Method of Statement	20	19-May-25	16-Jun-25	19-May-25 A	06-Oct-26	$0.00	$0.00	100%
Approvals		382	17-Jun-25	13-Aug-25	17-Jul-25 A	22-Dec-26	$0.00	$0.00	0%
S100086	Approval of Pre-commissioning/ Commissioning Plan/ Startup/ Testing / Handover Plan	10	03-Aug-25	13-Aug-25	12-Dec-26	22-Dec-26	$0.00	$0.00	100%
S100106	Approval of Method of Statement	10	17-Jun-25	28-Jun-25	17-Jul-25 A	12-Oct-26	$0.00	$0.00	100%
Engineering		265	03-Jul-25	03-Mar-26	20-Jul-25 A	14-Oct-26	$433,169.77	$144,180.58	100%
Shop Drawing		10	03-Jul-25	16-Jul-25	01-Mar-26 A	08-Oct-26	$0.00	$0.00	0%
Approvals		10	03-Jul-25	16-Jul-25	01-Mar-26 A	08-Oct-26	$0.00	$0.00	0%
A1630	Landscape details approval	10	03-Jul-25	16-Jul-25	01-Mar-26 A	08-Oct-26	$0.00	$0.00	100%
Material Submittal & Approval		265	03-Jul-25	03-Mar-26	20-Jul-25 A	14-Oct-26	$433,169.77	$144,180.58	100%
Long Lead Items		128	03-Jul-25	30-Jul-25	20-Jul-25 A	07-Oct-26	$311,534.63	$62,306.93	100%
Generators & Fuel Tanks - PS & Control Bldg backup power		128	03-Jul-25	30-Jul-25	20-Jul-25 A	07-Oct-26	$311,534.63	$62,306.93	100%
A102930	Material Submittal for Generators & Fuel Tanks - PS & Control Bldg backup power	13	03-Jul-25	21-Jul-25	20-Jul-25 A	06-Oct-26	$186,920.78	$37,384.16	100%
A102940	Material Approval for Generators & Fuel Tanks - PS & Control Bldg backup power	7	22-Jul-25	30-Jul-25	15-Dec-25 A	07-Oct-26	$124,613.85	$24,922.77	100%
Short Lead Items		48	18-Feb-26	03-Mar-26	21-Feb-26 A	14-Oct-26	$121,635.14	$81,873.65	100%
Interlock Tiles / Curbstone - Roads, Sidewalks, Landscape		7	18-Feb-26	03-Mar-26	21-Feb-26 A	13-Oct-26	$16,354.74	$8,177.37	100%
A103180	Material Approval for Interlock Tiles / Curbstone - Roads, Sidewalks, Landscape	7	18-Feb-26	03-Mar-26	21-Feb-26 A	13-Oct-26	$16,354.74	$8,177.37	100%
Landscaping Materials (Soil, Plants) - Final works, softscape		7	18-Feb-26	03-Mar-26	01-Apr-26 A	14-Oct-26	$105,280.40	$73,696.28	100%
A103200	Material Approval for Landscaping Materials (Soil, Plants) - Final works, softscape	7	18-Feb-26	03-Mar-26	01-Apr-26 A	14-Oct-26	$105,280.40	$73,696.28	100%
Procurement		421	23-Jul-25	31-Aug-26	13-Aug-25 A	01-Feb-27	15,318,372.1	$1,955,923.73	100%
Prequalification		105	19-Jan-26	29-Jan-26	13-Aug-25 A	07-Oct-26	$0.00	$0.00	0%
Short Lead Items		105	19-Jan-26	29-Jan-26	13-Aug-25 A	07-Oct-26	$0.00	$0.00	0%
Interlock Tiles / Curbstone - Roads, Sidewalks, Landscape		10	19-Jan-26	29-Jan-26	02-May-26 A	07-Oct-26	$0.00	$0.00	0%
A103560	Prequalification Approval for Interlock Tiles / Curbstone - Roads, Sidewalks, Landscape	10	19-Jan-26	29-Jan-26	02-May-26 A	07-Oct-26	$0.00	$0.00	100%
Landscaping Materials (Soil, Plants) - Final works, softscape		10	19-Jan-26	29-Jan-26	13-Aug-25 A	07-Oct-26	$0.00	$0.00	0%
A103580	Prequalification Approval for Landscaping Materials (Soil, Plants) - Final works, softscape	10	19-Jan-26	29-Jan-26	13-Aug-25 A	07-Oct-26	$0.00	$0.00	100%
Long Lead Items		367	23-Jul-25	31-Aug-26	24-Aug-25 A	30-Nov-26	13,452,257.8	$338,213.05	100%
Drainage Channel Covers (GRP / DI) - For storm and wastewater		155	11-Aug-25	04-Jan-26	17-Nov-25 A	04-Oct-26	8,032,142.3	$80,321.42	100%
A102570	Custom Clearance for Drainage Channel Covers (GRP / DI) - For storm and wastewater	10	21-Oct-25	01-Nov-25	17-Nov-25 A	03-Oct-26	$0.00	$0.00	100%
A102580	Staging Time for Drainage Channel Covers (GRP / DI) - For storm and wastewater	30	01-Dec-25	04-Jan-26	01-Jan-26 A	04-Oct-26	$0.00	$0.00	100%
A1230	Manufacturing for Drainage Channel Covers (GRP / DI) - For storm and wastewater	60	11-Aug-25	20-Oct-25	19-Nov-25 A	03-Oct-26	$0.00	$0.00	100%
A1240	Delivery for Drainage Channel Covers (GRP / DI) - For storm and wastewater	25	02-Nov-25	30-Nov-25	23-Nov-25 A	03-Oct-26	8,032,142.3	$80,321.42	100%
Control & Instrumentation Devices - Flow meters, pressure sensors		281	05-Aug-25	17-Dec-25	24-Aug-25 A	29-Oct-26	$285,073.41	$14,253.67	100%
A102610	Custom Clearance for Control & Instrumentation Devices - Flow meters, pressure sensor	5	28-Sep-25	02-Oct-25	26-Nov-25 A	04-Oct-26	$0.00	$0.00	100%
A102620	Staging Time for Control & Instrumentation Devices - Flow meters, pressure sensors	30	13-Nov-25	17-Dec-25	16-Apr-26 A	29-Oct-26	$0.00	$0.00	100%
A1530	Manufacturing for Control & Instrumentation Devices - Flow meters, pressure sensors	45	05-Aug-25	27-Sep-25	24-Aug-25 A	04-Oct-26	$0.00	$0.00	100%
A1570	Delivery for Control & Instrumentation Devices - Flow meters, pressure sensors	35	04-Oct-25	12-Nov-25	13-Apr-26 A	06-Oct-26	$285,073.41	$14,253.67	100%
Pumps (Sewage, Irrigation, Booster) - Especially for pumping stations		156	23-Jul-25	16-Dec-25	16-Oct-25 A	07-Oct-26	3,223,228.6	$128,929.15	100%
A102150	Manufacturing for Pumps (Sewage, Irrigation, Booster) - Especially for pumping stations	45	23-Jul-25	13-Sep-25	16-Oct-25 A	03-Oct-26	$0.00	$0.00	100%
A102170	Delivery for Pumps (Sewage, Irrigation, Booster) - Especially for pumping stations	45	20-Sep-25	11-Nov-25	05-Nov-25 A	05-Oct-26	3,223,228.6	$128,929.15	100%

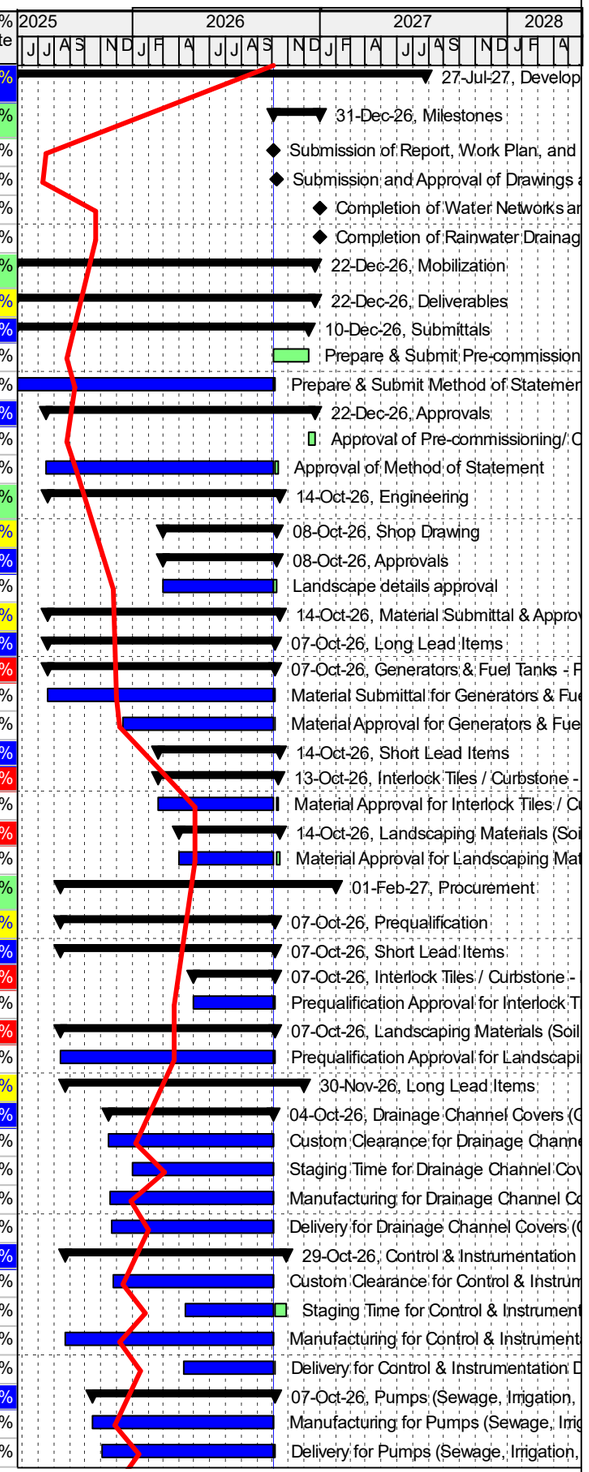


Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary

TASK filter: Schedule %.

© Oracle Corporation

Development of Phase One – Part Two – Third Industrial

Activity ID	Activity Name	Original Duration	BL Project Start	BL Project Finish	Start	Finish	Budgeted Total Cost	Remaining Total Cost	Schedule % Complete
A102630	Custom Clearance for Pumps (Sewage, Irrigation, Booster) - Especially for pumping stati	5	14-Sep-25	18-Sep-25	28-Nov-25 A	04-Oct-26	$0.00	$0.00	100%
A102640	Staging Time for Pumps (Sewage, Irrigation, Booster) - Especially for pumping stations	30	12-Nov-25	16-Dec-25	20-Jan-26 A	07-Oct-26	$0.00	$0.00	100%
Generators & Fuel Tanks - PS & Control Bldg backup power		181	05-Aug-25	13-Dec-25	08-Dec-25 A	26-Oct-26	1,911,813.4(	$114,708.81	100%
A102230	Manufacturing for Generators & Fuel Tanks - PS & Control Bldg backup power	55	05-Aug-25	08-Oct-25	08-Dec-25 A	11-Oct-26	$0.00	$0.00	100%
A102250	Delivery for Generators & Fuel Tanks - PS & Control Bldg backup power	21	15-Oct-25	08-Nov-25	10-Dec-25 A	12-Oct-26	1,911,813.4(	$114,708.81	100%
A102670	Custom Clearance for Generators & Fuel Tanks - PS & Control Bldg backup power	5	09-Oct-25	14-Oct-25	01-Jan-26 A	11-Oct-26	$0.00	$0.00	100%
A102680	Staging Time for Generators & Fuel Tanks - PS & Control Bldg backup power	30	09-Nov-25	13-Dec-25	04-Jul-26 A	26-Oct-26	$0.00	$0.00	100%
Odor Control Units - Sewer PS-specific		30	27-Jul-26	31-Aug-26	26-Oct-26	30-Nov-26	$0.00	$0.00	0%
A102720	Staging Time for Odor Control Units - Sewer PS-specific	30	27-Jul-26	31-Aug-26	26-Oct-26	30-Nov-26	$0.00	$0.00	100%
Short Lead Items		214	03-Mar-26	07-Jul-26	01-Jan-26 A	01-Feb-27	1,866,114.3(	$1,617,710.68	100%
Interlock Tiles / Curbstone - Roads, Sidewalks, Landscape		90	11-Mar-26	07-Jul-26	01-Jan-26 A	02-Nov-26	$250,912.80	$2,509.13	100%
A102380	Manufacturing for Interlock Tiles / Curbstone - Roads, Sidewalks, Landscape	30	11-Mar-26	23-Apr-26	01-Jan-26 A	13-Oct-26	$0.00	$0.00	100%
A102400	Delivery for Interlock Tiles / Curbstone - Roads, Sidewalks, Landscape	30	23-Apr-26	02-Jun-26	01-Apr-26 A	14-Oct-26	$250,912.80	$2,509.13	100%
A102820	Staging Time for Interlock Tiles / Curbstone - Roads, Sidewalks, Landscape	30	02-Jun-26	07-Jul-26	04-Jul-26 A	02-Nov-26	$0.00	$0.00	100%
Landscaping Materials (Soil, Plants) - Final works, softscape		94	03-Mar-26	07-Jul-26	14-Oct-26	01-Feb-27	1,615,201.5	$1,615,201.56	100%
A102350	Issue PO for Landscaping Materials (Soil, Plants) - Final works, softscape	4	03-Mar-26	10-Mar-26	14-Oct-26	19-Oct-26	$0.00	$0.00	100%
A102360	Manufacturing for Landscaping Materials (Soil, Plants) - Final works, softscape	60	11-Mar-26	02-Jun-26	19-Oct-26	28-Dec-26	$0.00	$0.00	100%
A102390	Delivery for Landscaping Materials (Soil, Plants) - Final works, softscape	30	02-Jun-26	07-Jul-26	28-Dec-26	01-Feb-27	1,615,201.5	$1,615,201.56	100%
Construction		601	19-Oct-25	25-Oct-26	03-Sep-25 A	27-Jul-27	)5,089,154.(	$33,777,353.53	98.85%
Zone 3		518	19-Oct-25	07-Oct-26	04-Oct-25 A	24-Jun-27	14,252,013.(	$17,106,904.96	99.98%
Sewerage Network Zone 3		334	19-Oct-25	25-Jun-26	13-Jan-26 A	17-Apr-27	4,595,438.7	$3,988,698.38	100%
Pipework: Supply, Installation, and Testing		164	14-Dec-25	27-Jan-26	23-Feb-26 A	26-Oct-26	$31,255.07	$16,669.37	100%
HDPE Pressure Pipes Installation (250mm–630mm)		164	14-Dec-25	27-Jan-26	23-Feb-26 A	26-Oct-26	$31,255.07	$16,669.37	100%
MOD-SWN-	Backfilling & Warning Tape HDPE for Sewerage Network Zone 3	15	13-Jan-26	27-Jan-26	12-Oct-26	26-Oct-26	$10,418.36	$10,418.36	100%
MOD-SWN-	Test (Pressure - Slope) HDPE for Sewerage Network Zone 3	15	14-Dec-25	28-Dec-25	23-Feb-26 A	05-Oct-26	$10,418.36	$2,083.67	100%
MOD-SWN-	Coating / Wrapping HDPE for Sewerage Network Zone 3	15	29-Dec-25	12-Jan-26	01-Mar-26 A	11-Oct-26	$10,418.36	$4,167.34	100%
Fittings and Valves		27	14-Dec-25	13-Jan-26	03-Oct-26	02-Nov-26	$30,711.20	$30,711.20	100%
MOD-SWN-FV-	Supply & Installation of HDPE Elbows for Sewerage Network Zone 3	6	14-Dec-25	20-Dec-25	03-Oct-26	08-Oct-26	$6,826.21	$6,826.21	100%
MOD-SWN-FV-	Gate Valves Installation for Sewerage Network Zone 3	4	21-Dec-25	24-Dec-25	10-Oct-26	13-Oct-26	$4,830.30	$4,830.30	100%
MOD-SWN-FV-	Drain Valves Installation for Sewerage Network Zone 3	4	25-Dec-25	29-Dec-25	14-Oct-26	18-Oct-26	$4,392.82	$4,392.82	100%
MOD-SWN-FV-	Air Breather & Air Release Valves Installation for Sewerage Network Zone 3	10	30-Dec-25	10-Jan-26	19-Oct-26	29-Oct-26	$11,590.74	$11,590.74	100%
MOD-SWN-FV-	Jointing & Piping Accessories Installation for Sewerage Network Zone 3	3	11-Jan-26	13-Jan-26	31-Oct-26	02-Nov-26	$3,071.12	$3,071.12	100%
Valve & Flow Meter Chambers		87	19-Oct-25	10-Feb-26	08-Jun-26 A	14-Dec-26	$49,924.39	$31,970.65	100%
Valve Chambers Construction		58	19-Oct-25	04-Jan-26	08-Jun-26 A	16-Nov-26	$6,894.06	$4,033.03	100%
MOD-SWN-	Backfilling Valve Chamber for Sewerage Network Zone 3	15	21-Dec-25	04-Jan-26	01-Nov-26	16-Nov-26	$1,378.81	$1,378.81	100%
MOD-SWN-	Excavation Valve Chamber for Sewerage Network Zone 3	21	19-Oct-25	08-Nov-25	08-Jun-26 A	11-Oct-26	$1,034.11	$413.64	100%
MOD-SWN-	Lean Concrete / Bedding Valve Chamber for Sewerage Network Zone 3	21	09-Nov-25	29-Nov-25	22-Jul-26 A	21-Oct-26	$689.41	$344.70	100%
MOD-SWN-	Test Valve Chamber for Sewerage Network Zone 3	15	06-Dec-25	20-Dec-25	04-Aug-26 A	01-Nov-26	$689.41	$344.70	100%
MOD-SWN-	Valve Chambers Construction Valve Chamber for Sewerage Network Zone 3	6	30-Nov-25	05-Dec-25	31-Jul-26 A	24-Oct-26	$3,102.33	$1,551.16	100%
Water Drain Chambers Construction		75	19-Oct-25	23-Jan-26	16-Jun-26 A	03-Dec-26	$22,394.28	$13,660.51	100%
MOD-SWN-	Backfilling Water Drain Chamber for Sewerage Network Zone 3	15	09-Jan-26	23-Jan-26	18-Nov-26	03-Dec-26	$4,478.86	$4,478.86	100%
MOD-SWN-	Excavation Water Drain Chamber for Sewerage Network Zone 3	21	19-Oct-25	08-Nov-25	16-Jun-26 A	09-Oct-26	$3,359.14	$1,007.74	100%
MOD-SWN-	Lean Concrete / Bedding Water Drain Chamber for Sewerage Network Zone 3	21	09-Nov-25	29-Nov-25	23-Jun-26 A	17-Oct-26	$2,239.43	$895.77	100%
MOD-SWN-	Test Water Drain Chamber for Sewerage Network Zone 3	15	25-Dec-25	08-Jan-26	03-Nov-26	18-Nov-26	$2,239.43	$2,239.43	100%
MOD-SWN-	Water Drain Chambers Construction Water Drain Chamber for Sewerage Network Zone 3	19	06-Dec-25	24-Dec-25	01-Jul-26 A	03-Nov-26	$10,077.42	$5,038.71	100%
Discharge Chambers Construction		82	19-Oct-25	05-Feb-26	01-Jul-26 A	09-Dec-26	$15,643.62	$9,933.70	100%
MOD-SWN-	Backfilling Discharge Chamber for Sewerage Network Zone 3	15	22-Jan-26	05-Feb-26	24-Nov-26	09-Dec-26	$3,128.72	$3,128.72	100%
MOD-SWN-	Excavation Discharge Chamber for Sewerage Network Zone 3	21	19-Oct-25	08-Nov-25	01-Jul-26 A	11-Oct-26	$2,346.54	$938.62	100%
MOD-SWN-	Lean Concrete / Bedding Discharge Chamber for Sewerage Network Zone 3	21	09-Nov-25	29-Nov-25	15-Jul-26 A	21-Oct-26	$1,564.36	$782.18	100%

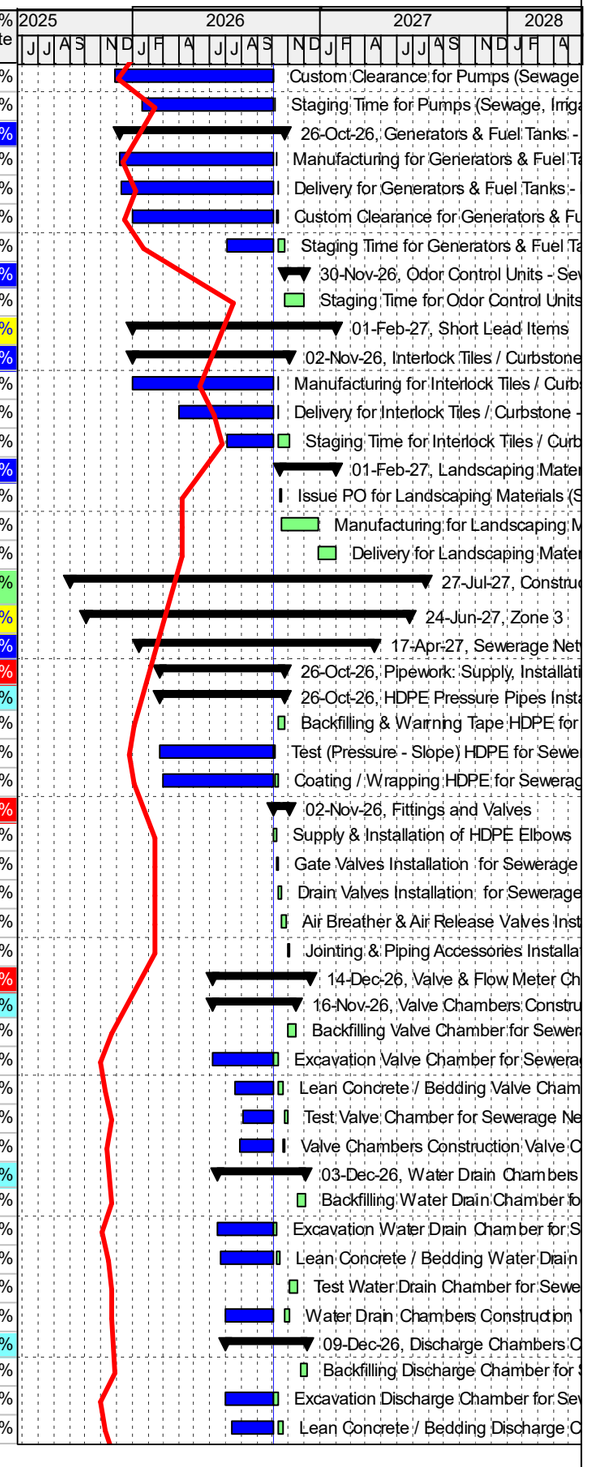


Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary

TASK filter: Schedule %.

© Oracle Corporation

Development of Phase One – Part Two – Third Industrial

Activity ID	Activity Name	Original Duration	BL Project Start	BL Project Finish	Start	Finish	Budgeted Total Cost	Remaining Total Cost	Schedule % Complete
MOD-SWN-	Test Discharge Chamber for Sewerage Network Zone 3	15	07-Jan-26	21-Jan-26	09-Nov-26	24-Nov-26	$1,564.36	$1,564.36	100%
MOD-SWN-	Discharge Chambers Construction Discharge Chamber for Sewerage Network Zone 3	13	25-Dec-25	06-Jan-26	01-Aug-26 A	09-Nov-26	$7,039.63	$3,519.81	100%
Flow Meter Chambers Construction		87	19-Oct-25	10-Feb-26	14-Jul-26 A	14-Dec-26	$4,992.44	$4,343.42	100%
MOD-SWN-	Backfilling Flow Meter Chamber for Sewerage Network Zone 3	15	27-Jan-26	10-Feb-26	29-Nov-26	14-Dec-26	$998.49	$998.49	100%
MOD-SWN-	Excavation Flow Meter Chamber for Sewerage Network Zone 3	21	19-Oct-25	08-Nov-25	14-Jul-26 A	11-Oct-26	$748.87	$299.55	100%
MOD-SWN-	Lean Concrete / Bedding Flow Meter Chamber for Sewerage Network Zone 3	21	09-Nov-25	29-Nov-25	29-Jul-26 A	23-Oct-26	$499.24	$299.55	100%
MOD-SWN-	Test Flow Meter Chamber for Sewerage Network Zone 3	15	12-Jan-26	26-Jan-26	14-Nov-26	29-Nov-26	$499.24	$499.24	100%
MOD-SWN-	Flow Meter Chambers Construction Flow Meter Chamber for Sewerage Network Zone 3	5	07-Jan-26	11-Jan-26	09-Nov-26	14-Nov-26	$2,246.60	$2,246.60	100%
Manholes		174	19-Oct-25	04-Mar-26	02-Feb-26 A	03-Dec-26	$426,556.55	$206,739.05	100%
1500mm GRP Manholes (Standard & Backdrop)		161	19-Oct-25	09-Feb-26	02-Feb-26 A	20-Nov-26	$400,264.86	$192,127.13	100%
MOD-SWN-	1500mm GRP Manholes (Standard & Backdrop) 1.5m GRP for Sewerage Network Zone	21	21-Dec-25	10-Jan-26	18-Mar-26 A	19-Oct-26	$180,119.19	$54,035.76	100%
MOD-SWN-	Backfilling 1.5m GRP for Sewerage Network Zone 3	15	26-Jan-26	09-Feb-26	05-Nov-26	20-Nov-26	$80,052.97	$80,052.97	100%
MOD-SWN-	Excavation 1.5m GRP for Sewerage Network Zone 3	21	19-Oct-25	08-Nov-25	02-Feb-26 A	05-Oct-26	$60,039.73	$6,003.97	100%
MOD-SWN-	Lean Concrete / Bedding 1.5m GRP for Sewerage Network Zone 3	21	09-Nov-25	29-Nov-25	10-Mar-26 A	11-Oct-26	$40,026.49	$12,007.95	100%
MOD-SWN-	Test 1.5m GRP for Sewerage Network Zone 3	15	11-Jan-26	25-Jan-26	21-Oct-26	05-Nov-26	$40,026.49	$40,026.49	100%
1800mm GRP Manholes (Standard & Backdrop)		168	19-Oct-25	26-Feb-26	17-Feb-26 A	27-Nov-26	$19,968.17	$9,584.72	100%
MOD-SWN-	1800mm GRP Manholes (Standard & Backdrop) 1.8m GRP for Sewerage Network Zone	17	11-Jan-26	27-Jan-26	04-Mar-26 A	26-Oct-26	$8,985.68	$2,695.70	100%
MOD-SWN-	Backfilling 1.8m GRP for Sewerage Network Zone 3	15	12-Feb-26	26-Feb-26	12-Nov-26	27-Nov-26	$3,993.63	$3,993.63	100%
MOD-SWN-	Excavation 1.8m GRP for Sewerage Network Zone 3	21	19-Oct-25	08-Nov-25	17-Feb-26 A	05-Oct-26	$2,995.23	$299.52	100%
MOD-SWN-	Lean Concrete / Bedding 1.8m GRP for Sewerage Network Zone 3	21	09-Nov-25	29-Nov-25	24-Feb-26 A	11-Oct-26	$1,996.82	$599.05	100%
MOD-SWN-	Test 1.8m GRP for Sewerage Network Zone 3	15	28-Jan-26	11-Feb-26	28-Oct-26	12-Nov-26	$1,996.82	$1,996.82	100%
2000mm GRP Manholes (Standard & Backdrop)		174	19-Oct-25	04-Mar-26	15-Feb-26 A	03-Dec-26	$6,323.52	$5,027.20	100%
MOD-SWN-	2000mm GRP Manholes (Standard & Backdrop) 2m GRP for Sewerage Network Zone 3	6	28-Jan-26	02-Feb-26	28-Oct-26	03-Nov-26	$2,845.59	$2,845.59	100%
MOD-SWN-	Backfilling 2m GRP for Sewerage Network Zone 3	15	18-Feb-26	04-Mar-26	18-Nov-26	03-Dec-26	$1,264.70	$1,264.70	100%
MOD-SWN-	Excavation 2m GRP for Sewerage Network Zone 3	21	19-Oct-25	08-Nov-25	15-Feb-26 A	05-Oct-26	$948.53	$94.85	100%
MOD-SWN-	Lean Concrete / Bedding 2m GRP for Sewerage Network Zone 3	21	09-Nov-25	29-Nov-25	04-Mar-26 A	11-Oct-26	$632.35	$189.71	100%
MOD-SWN-	Test 2m GRP for Sewerage Network Zone 3	15	03-Feb-26	17-Feb-26	03-Nov-26	18-Nov-26	$632.35	$632.35	100%
Pumping Stations		152	06-Nov-25	25-Jun-26	13-Jan-26 A	17-Apr-27	4,056,991.5	$3,702,608.09	100%
In-Line Booster Stations		63	01-Dec-25	11-Feb-26	03-Oct-26	14-Dec-26	1,968,220.0	$1,968,220.09	100%
MOD-SWN-	In-Line Booster Stations - Mechanical Works for Sewerage Network Zone 3	21	25-Dec-25	18-Jan-26	27-Oct-26	19-Nov-26	$656,073.36	$656,073.36	100%
MOD-SWN-	In-Line Booster Stations - Electrical Works for Sewerage Network Zone 3	21	19-Jan-26	11-Feb-26	21-Nov-26	14-Dec-26	$656,073.36	$656,073.36	100%
MOD-SWN-	In-Line Booster Stations - Civil Works for Sewerage Network Zone 3	21	01-Dec-25	24-Dec-25	03-Oct-26	26-Oct-26	$656,073.36	$656,073.36	100%
Engine/Motor Control Center Buildings		8	06-Nov-25	08-Dec-25	03-Oct-26	11-Oct-26	$45,941.19	$45,941.19	100%
MOD-SWN-	MCC Building – PS3 for Sewerage Network Zone 3	1	06-Nov-25	06-Nov-25	03-Oct-26	03-Oct-26	$3,888.46	$3,888.46	100%
MOD-SWN-	MCC Building – PS4 for Sewerage Network Zone 3	7	01-Dec-25	08-Dec-25	04-Oct-26	11-Oct-26	$42,052.73	$42,052.73	100%
Valves and Fittings (General Supply & Installation)		8	18-Dec-25	27-Dec-25	30-Aug-26 A	05-Nov-26	$43,723.31	$34,978.65	100%
MOD-SWN-	Valves, fittings, flow meters – PS3 for Sewerage Network Zone 3	2	18-Dec-25	20-Dec-25	30-Aug-26 A	31-Oct-26	$11,924.59	$9,539.67	100%
MOD-SWN-	Valves, fittings, flow meters – PS4 for Sewerage Network Zone 3	3	21-Dec-25	23-Dec-25	01-Sep-26 A	03-Nov-26	$14,516.89	$11,613.51	100%
MOD-SWN-	35mm SS 316 mesh network – PS4 for Sewerage Network Zone 3	3	24-Dec-25	27-Dec-25	08-Sep-26 A	05-Nov-26	$17,281.83	$13,825.46	100%
Tank with Canopy		12	28-Dec-25	10-Jan-26	05-Nov-26	19-Nov-26	$720,080.25	$720,080.25	100%
MOD-SWN-	Tank with canopy (per specs/drawings) - PS4 for Sewerage Network Zone 3	12	28-Dec-25	10-Jan-26	05-Nov-26	19-Nov-26	$720,080.25	$720,080.25	100%
Pump Well and Valve Chambers		77	11-Jan-26	14-May-26	19-Nov-26	27-Feb-27	$773,616.05	$773,616.05	100%
MOD-SWN-	Pump well & valve chamber structure – PS3 (2 wells, 5x5m, 11m depth) for Sewerage N	21	11-Jan-26	03-Feb-26	19-Nov-26	14-Dec-26	$254,390.01	$254,390.01	100%
MOD-SWN-	Concrete wall (5x5x1m) inside PS3 well for Sewerage Network Zone 3	4	06-Apr-26	11-Apr-26	14-Dec-26	19-Dec-26	$19,816.65	$19,816.65	100%
MOD-SWN-	Valve chamber – PS3 for Sewerage Network Zone 3	20	11-Apr-26	04-May-26	19-Dec-26	11-Jan-27	$117,056.19	$117,056.19	100%
MOD-SWN-	Flow meter chamber – PS3 for Sewerage Network Zone 3	9	04-May-26	14-May-26	11-Jan-27	21-Jan-27	$54,872.10	$54,872.10	100%
MOD-SWN-	Pump well & valve chamber structure – PS4 (1 well, 4m, 11m depth) for Sewerage Netw	22	04-Feb-26	11-Mar-26	14-Dec-26	09-Jan-27	$129,464.76	$129,464.76	100%
MOD-SWN-	Valve chamber – PS4 for Sewerage Network Zone 3	21	12-Mar-26	13-Apr-26	09-Jan-27	02-Feb-27	$124,372.20	$124,372.20	100%
MOD-SWN-	Flow meter chamber – PS4 for Sewerage Network Zone 3	13	13-Apr-26	28-Apr-26	02-Feb-27	27-Feb-27	$73,644.14	$73,644.14	100%
Odor Control System Base/Plinth		6	03-Jun-26	10-Jun-26	08-Apr-27	15-Apr-27	$16,590.51	$16,590.51	100%

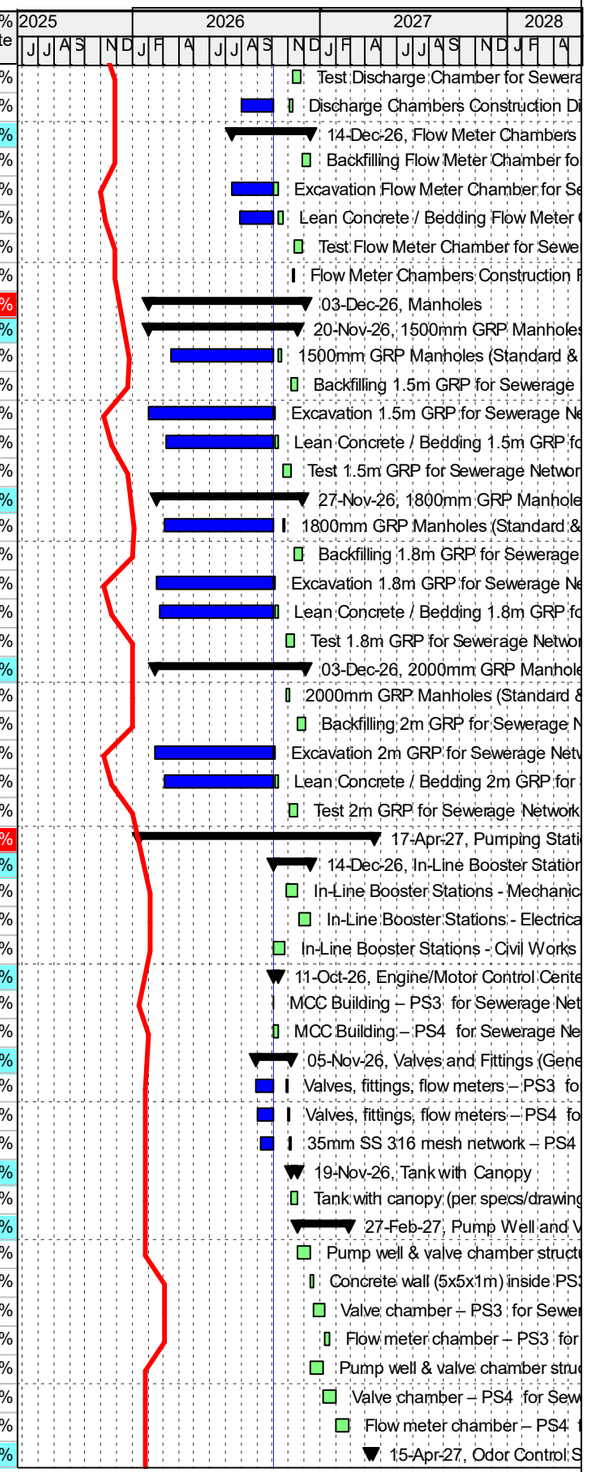


Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary

TASK filter: Schedule %.

© Oracle Corporation

Development of Phase One – Part Two – Third Industrial

Activity ID	Activity Name	Original Duration	BL Project Start	BL Project Finish	Start	Finish	Budgeted Total Cost	Remaining Total Cost	Schedule % Complete
MOD-SWN-	Concrete plinth below odor control – PS3 & PS4 for Sewerage Network Zone 3	6	03-Jun-26	10-Jun-26	08-Apr-27	15-Apr-27	$16,590.51	$16,590.51	100%
Lighting Works		13	10-Jun-26	25-Jun-26	13-Jan-26 A	17-Apr-27	$384,043.12	$38,404.31	100%
MOD-SWN-	250W Flood Light installation – PS3 & PS4 for Sewerage Network Zone 3	13	10-Jun-26	25-Jun-26	13-Jan-26 A	17-Apr-27	$384,043.12	$38,404.31	100%
Duct Works		7	28-Apr-26	06-May-26	27-Feb-27	16-Mar-27	$15,220.07	$15,220.07	100%
MOD-SWN-	uPVC duct Track 1 – PS3 & PS4 for Sewerage Network Zone 3	1	28-Apr-26	29-Apr-26	27-Feb-27	28-Feb-27	$2,760.41	$2,760.41	100%
MOD-SWN-	uPVC duct Track 2 – PS3 & PS4 for Sewerage Network Zone 3	2	29-Apr-26	02-May-26	28-Feb-27	04-Mar-27	$3,185.08	$3,185.08	100%
MOD-SWN-	uPVC duct Track 8 – PS3 & PS4 for Sewerage Network Zone 3	4	02-May-26	06-May-26	04-Mar-27	16-Mar-27	$9,274.58	$9,274.58	100%
Grounding Works		3	06-May-26	10-May-26	16-Mar-27	20-Mar-27	$7,603.32	$7,603.32	100%
MOD-SWN-	Grounding pit – PS3 & PS4 for Sewerage Network Zone 3	1	06-May-26	07-May-26	16-Mar-27	17-Mar-27	$1,690.17	$1,690.17	100%
MOD-SWN-	600x600 Cable pull pit – PS3 & PS4 for Sewerage Network Zone 3	2	07-May-26	10-May-26	17-Mar-27	20-Mar-27	$5,913.15	$5,913.15	100%
Landscaping / Interlocking Tiles		21	10-May-26	08-Jun-26	20-Mar-27	13-Apr-27	$61,674.68	$61,674.68	100%
MOD-SWN-	Building perimeter interlock tiles for Sewerage Network Zone 3	17	10-May-26	03-Jun-26	20-Mar-27	08-Apr-27	$50,952.81	$50,952.81	100%
MOD-SWN-	Entrance road paving tiles for Sewerage Network Zone 3	4	03-Jun-26	08-Jun-26	08-Apr-27	13-Apr-27	$10,721.87	$10,721.87	100%
Pumping Station Internal Drainage Network		7	10-May-26	18-May-26	20-Mar-27	28-Mar-27	$20,278.98	$20,278.98	100%
MOD-SWN-	Internal surface drainage channels for Sewerage Network Zone 3	7	10-May-26	18-May-26	20-Mar-27	28-Mar-27	$20,278.98	$20,278.98	100%
Rainwater Drainage Network Zone 3		286	19-Oct-25	18-Jan-26	05-Jan-26 A	26-Nov-26	9,430,843.9	$3,240,566.18	100%
Pipe Laying Works		261	19-Oct-25	18-Jan-26	05-Jan-26 A	01-Nov-26	$470,742.02	$88,034.52	100%
Supply & Installation of uPVC Pipes (250–300mm dia)		153	19-Oct-25	13-Dec-25	05-Jan-26 A	09-Oct-26	$376,944.63	$47,118.08	100%
MOD-RWN-	Excavation to required depth UPVC for Rainwater Drainage Network Zone 3	21	19-Oct-25	08-Nov-25	05-Jan-26 A	04-Oct-26	$75,388.93	$3,769.45	100%
MOD-RWN-	Lean Concrete / Bedding UPVC for Rainwater Drainage Network Zone 3	5	09-Nov-25	13-Nov-25	05-Jan-26 A	04-Oct-26	$18,847.23	$942.36	100%
MOD-RWN-	Laying of uPVC pipe UPVC for Rainwater Drainage Network Zone 3	19	14-Nov-25	02-Dec-25	05-Jan-26 A	05-Oct-26	$169,625.08	$8,481.25	100%
MOD-RWN-	Coating / Wrapping UPVC for Rainwater Drainage Network Zone 3	2	06-Dec-25	07-Dec-25	23-Feb-26 A	06-Oct-26	$37,694.46	$7,538.89	100%
MOD-RWN-	Test (Pressure-slope) UPVC for Rainwater Drainage Network Zone 3	3	03-Dec-25	05-Dec-25	03-Feb-26 A	05-Oct-26	$37,694.46	$7,538.89	100%
MOD-RWN-	Backfilling & Warning Tape UPVC for Rainwater Drainage Network Zone 3	8	06-Dec-25	13-Dec-25	21-Jun-26 A	09-Oct-26	$37,694.46	$18,847.23	100%
Supply & Installation of GRP Pipes (350–800mm dia)		42	08-Dec-25	18-Jan-26	01-Jun-26 A	23-Oct-26	$51,668.82	$25,834.41	100%
MOD-RWN-	Test (Pressure-slope) GRP for Rainwater Drainage Network Zone 3	11	08-Dec-25	18-Dec-25	01-Jun-26 A	08-Oct-26	$17,222.94	$8,611.47	100%
MOD-RWN-	Coating / Wrapping GRP for Rainwater Drainage Network Zone 3	21	19-Dec-25	08-Jan-26	01-Jul-26 A	18-Oct-26	$17,222.94	$8,611.47	100%
MOD-RWN-	Backfilling & compaction GRP for Rainwater Drainage Network Zone 3	10	09-Jan-26	18-Jan-26	01-Aug-26 A	23-Oct-26	$17,222.94	$8,611.47	100%
uPVC Connection Pipes (150mm dia)		261	19-Oct-25	05-Jan-26	05-Jan-26 A	01-Nov-26	$42,128.57	$15,082.03	100%
MOD-RWN-	Excavate short trench paths UPVC Con. for Rainwater Drainage Network Zone 3	5	19-Oct-25	23-Oct-25	05-Jan-26 A	03-Oct-26	$8,425.71	$421.29	100%
MOD-RWN-	Lean Concrete / bedding material UPVC Con. for Rainwater Drainage Network Zone 3	3	24-Oct-25	26-Oct-25	05-Jan-26 A	03-Oct-26	$2,106.43	$126.39	100%
MOD-RWN-	Lay & connect UPVC Con. for Rainwater Drainage Network Zone 3	8	03-Dec-25	10-Dec-25	05-Jan-26 A	06-Oct-26	$18,957.86	$1,895.79	100%
MOD-RWN-	Test (Pressure-slope) UPVC Con. for Rainwater Drainage Network Zone 3	3	11-Dec-25	13-Dec-25	06-Oct-26	09-Oct-26	$4,212.86	$4,212.86	100%
MOD-RWN-	Backfilling & compaction UPVC Con. for Rainwater Drainage Network Zone 3	2	04-Jan-26	05-Jan-26	30-Oct-26	01-Nov-26	$4,212.86	$4,212.86	100%
MOD-RWN-	Coating / Wrapping UPVC Con. for Rainwater Drainage Network Zone 3	21	14-Dec-25	03-Jan-26	09-Oct-26	30-Oct-26	$4,212.86	$4,212.86	100%
Precast Concrete Box Culverts		71	15-Nov-25	18-Jan-26	05-Sep-26 A	26-Nov-26	$768,525.45	$715,523.70	100%
Box Culverts (500x500mm to 3500x800mm)		71	15-Nov-25	18-Jan-26	05-Sep-26 A	26-Nov-26	$768,525.45	$715,523.70	100%
MOD-RWN-	Dewatering and trench shoring Box culvert for Rainwater Drainage Network Zone 3	10	15-Nov-25	02-Dec-25	05-Sep-26 A	11-Oct-26	$212,007.02	$159,005.27	100%
MOD-RWN-	Bedding preparation (gravel/lean concrete) Box culvert for Rainwater Drainage Network Z	4	02-Dec-25	07-Dec-25	11-Oct-26	15-Oct-26	$79,502.63	$79,502.63	100%
MOD-RWN-	Installation of box culvert units Box culvert for Rainwater Drainage Network Zone 3	10	07-Dec-25	18-Dec-25	15-Oct-26	27-Oct-26	$318,010.53	$318,010.53	100%
MOD-RWN-	Alignment and joint sealing Box culvert for Rainwater Drainage Network Zone 3	4	18-Dec-25	23-Dec-25	27-Oct-26	01-Nov-26	$37,101.23	$37,101.23	100%
MOD-RWN-	Construct headwalls/wing walls (if needed) Box culvert for Rainwater Drainage Network Z	12	23-Dec-25	06-Jan-26	01-Nov-26	15-Nov-26	$53,001.76	$53,001.76	100%
MOD-RWN-	Backfilling and compaction Box culvert for Rainwater Drainage Network Zone 3	7	06-Jan-26	14-Jan-26	15-Nov-26	23-Nov-26	$37,101.23	$37,101.23	100%
MOD-RWN-	Surface finishing Box culvert for Rainwater Drainage Network Zone 3	3	14-Jan-26	18-Jan-26	23-Nov-26	26-Nov-26	$31,801.05	$31,801.05	100%
Manholes		36	07-Dec-25	18-Jan-26	15-Oct-26	26-Nov-26	$780,038.12	$780,038.12	100%
Circular GRP Manholes (1200–1800mm dia)		32	07-Dec-25	13-Jan-26	15-Oct-26	22-Nov-26	$228,708.76	$228,708.76	100%
MOD-RWN-	Excavate to full manhole depth Circular Manhole for Rainwater Drainage Network Zone 3	7	07-Dec-25	15-Dec-25	15-Oct-26	24-Oct-26	$8,004.81	$8,004.81	100%
MOD-RWN-	Dewatering and safety barriers Circular Manhole for Rainwater Drainage Network Zone 3	6	15-Dec-25	22-Dec-25	24-Oct-26	31-Oct-26	$69,756.17	$69,756.17	100%
MOD-RWN-	Concrete base construction Circular Manhole for Rainwater Drainage Network Zone 3	2	22-Dec-25	24-Dec-25	31-Oct-26	02-Nov-26	$68,612.63	$68,612.63	100%
MOD-RWN-	Install GRP manhole shaft sections Circular Manhole for Rainwater Drainage Network Zo	7	24-Dec-25	01-Jan-26	02-Nov-26	10-Nov-26	$57,177.19	$57,177.19	100%

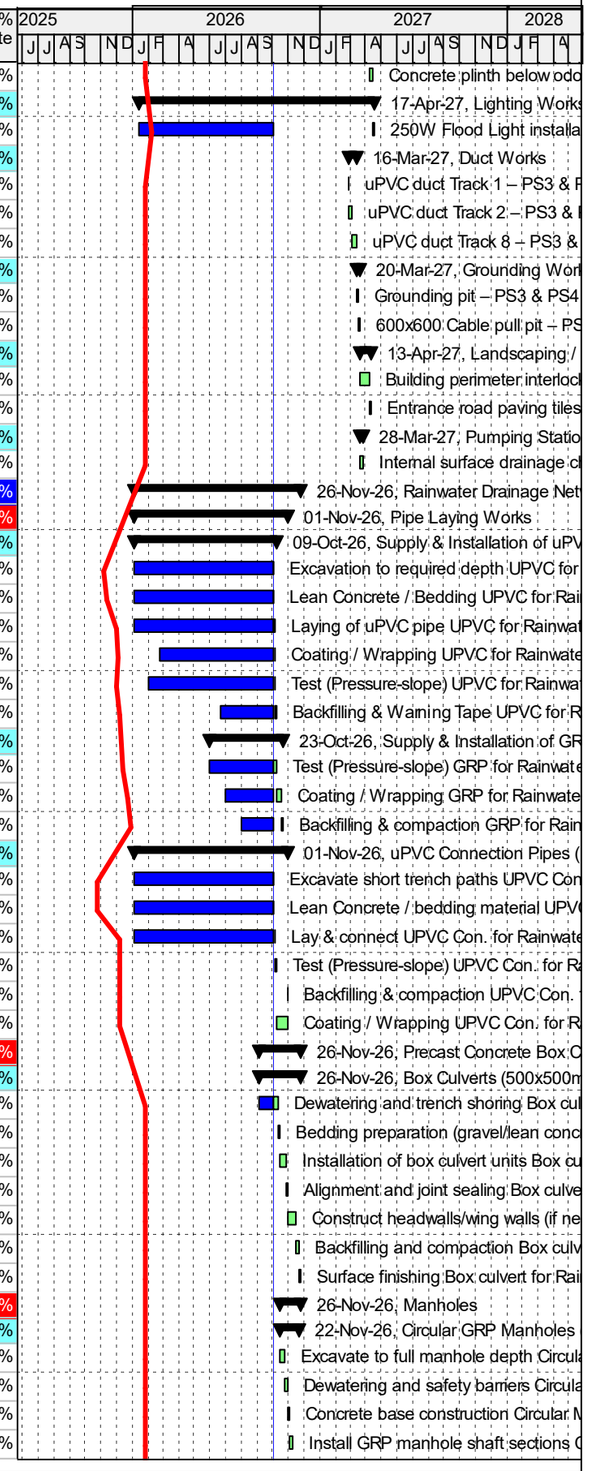


Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary

TASK filter: Schedule %.

© Oracle Corporation

Development of Phase One – Part Two – Third Industrial

Activity ID	Activity Name	Original Duration	BL Project Start	BL Project Finish	Start	Finish	Budgeted Total Cost	Remaining Total Cost	Schedule % Complete
MOD-RWN-	Place slab and cover frame Circular Manhole for Rainwater Drainage Network Zone 3	6	01-Jan-26	08-Jan-26	10-Nov-26	17-Nov-26	$17,153.16	$17,153.16	100%
MOD-RWN-	Waterproofing Circular Manhole for Rainwater Drainage Network Zone 3	2	08-Jan-26	11-Jan-26	17-Nov-26	19-Nov-26	$4,574.18	$4,574.18	100%
MOD-RWN-	Backfilling and compaction Circular Manhole for Rainwater Drainage Network Zone 3	2	11-Jan-26	13-Jan-26	19-Nov-26	22-Nov-26	$3,430.63	$3,430.63	100%
Concrete Manholes for 1500x1500 Box Pipes		32	07-Dec-25	13-Jan-26	15-Oct-26	22-Nov-26	$354,504.29	$354,504.29	100%
MOD-RWN-	Excavation Concrete Manhole 1.5x1.5 for Rainwater Drainage Network Zone 3	6	07-Dec-25	14-Dec-25	15-Oct-26	22-Oct-26	$12,407.65	$12,407.65	100%
MOD-RWN-	Base slab and wall shuttering Concrete Manhole 1.5x1.5 for Rainwater Drainage Networl	4	14-Dec-25	18-Dec-25	22-Oct-26	27-Oct-26	$108,123.81	$108,123.81	100%
MOD-RWN-	Wall reinforcement and casting Concrete Manhole 1.5x1.5 for Rainwater Drainage Netw	8	18-Dec-25	28-Dec-25	27-Oct-26	05-Nov-26	$106,351.29	$106,351.29	100%
MOD-RWN-	Roof slab with openings Concrete Manhole 1.5x1.5 for Rainwater Drainage Network Zon	4	28-Dec-25	01-Jan-26	05-Nov-26	10-Nov-26	$88,626.07	$88,626.07	100%
MOD-RWN-	Masonry/benching works inside Concrete Manhole 1.5x1.5 for Rainwater Drainage Netw	5	01-Jan-26	07-Jan-26	10-Nov-26	16-Nov-26	$26,587.82	$26,587.82	100%
MOD-RWN-	Install cover and frame Concrete Manhole 1.5x1.5 for Rainwater Drainage Network Zone	2	07-Jan-26	10-Jan-26	16-Nov-26	18-Nov-26	$7,090.09	$7,090.09	100%
MOD-RWN-	Backfill in layers Concrete Manhole 1.5x1.5 for Rainwater Drainage Network Zone 3	3	10-Jan-26	13-Jan-26	18-Nov-26	22-Nov-26	$5,317.56	$5,317.56	100%
Concrete Manholes for 1000x1000 Box Pipes		36	07-Dec-25	18-Jan-26	15-Oct-26	26-Nov-26	$196,825.07	$196,825.07	100%
MOD-RWN-	Excavation Concrete Manhole 1x1 for Rainwater Drainage Network Zone 3	6	07-Dec-25	14-Dec-25	15-Oct-26	22-Oct-26	$6,888.88	$6,888.88	100%
MOD-RWN-	Base slab and wall shuttering Concrete Manhole 1x1 for Rainwater Drainage Network Zo	4	14-Dec-25	18-Dec-25	22-Oct-26	27-Oct-26	$60,031.65	$60,031.65	100%
MOD-RWN-	Wall reinforcement and casting Concrete Manhole 1x1 for Rainwater Drainage Network Z	6	18-Dec-25	25-Dec-25	27-Oct-26	03-Nov-26	$59,047.52	$59,047.52	100%
MOD-RWN-	Roof slab with openings Concrete Manhole 1x1 for Rainwater Drainage Network Zone 3	4	25-Dec-25	30-Dec-25	03-Nov-26	08-Nov-26	$49,206.27	$49,206.27	100%
MOD-RWN-	Masonry/benching works inside Concrete Manhole 1x1 for Rainwater Drainage Network Z	7	30-Dec-25	07-Jan-26	08-Nov-26	16-Nov-26	$14,761.88	$14,761.88	100%
MOD-RWN-	Install cover and frame Concrete Manhole 1x1 for Rainwater Drainage Network Zone 3	4	07-Jan-26	12-Jan-26	16-Nov-26	21-Nov-26	$3,936.50	$3,936.50	100%
MOD-RWN-	Backfill in layers Concrete Manhole 1x1 for Rainwater Drainage Network Zone 3	5	12-Jan-26	18-Jan-26	21-Nov-26	26-Nov-26	$2,952.38	$2,952.38	100%
Chambers and Catch Basins		114	29-Dec-25	17-Jan-26	16-Mar-26 A	21-Oct-26	$74,226.71	$27,865.27	100%
Gully Outfalls		33	29-Dec-25	05-Jan-26	16-Mar-26 A	17-Oct-26	$31,336.47	$9,490.47	100%
MOD-RWN-	Provide slope protection (riprap) Gully Outfall for Rainwater Drainage Network Zone 3	4	29-Dec-25	03-Jan-26	16-Mar-26 A	15-Oct-26	$13,429.92	$537.20	100%
MOD-RWN-	Compact and shape terrain Gully Outfall for Rainwater Drainage Network Zone 3	2	03-Jan-26	05-Jan-26	23-Jun-26 A	17-Oct-26	$17,906.55	$8,953.28	100%
Rainwater Catch Basins		2	07-Jan-26	10-Jan-26	01-Jul-26 A	15-Oct-26	$26,080.25	$1,564.82	100%
MOD-RWN-	Backfill and surface finish Catch Basin for Rainwater Drainage Network Zone 3	2	07-Jan-26	10-Jan-26	01-Jul-26 A	15-Oct-26	$26,080.25	$1,564.82	100%
Precast Chambers for Absorption Pits		5	11-Jan-26	17-Jan-26	15-Oct-26	21-Oct-26	$16,809.98	$16,809.98	100%
MOD-RWN-	Backfill and compact Absorption Pit for Rainwater Drainage Network Zone 3	5	11-Jan-26	17-Jan-26	15-Oct-26	21-Oct-26	$16,809.98	$16,809.98	100%
Gully Outfalls to Swales		141	28-Dec-25	18-Jan-26	09-Feb-26 A	05-Nov-26	$162,746.41	$69,344.12	100%
Gully Outfalls to Swales		127	31-Dec-25	17-Jan-26	09-Feb-26 A	20-Oct-26	$127,366.76	$33,964.47	100%
MOD-RWN-	Excavate outfall channel Gully Outfall to Swales for Rainwater Drainage Network Zone 3	4	31-Dec-25	05-Jan-26	09-Feb-26 A	15-Oct-26	$28,303.72	$2,830.37	100%
MOD-RWN-	Place concrete apron or pipes Gully Outfall to Swales for Rainwater Drainage Network Zc	5	05-Jan-26	11-Jan-26	01-Mar-26 A	17-Oct-26	$63,683.38	$12,736.68	100%
MOD-RWN-	Provide slope protection (riprap) Gully Outfall to Swales for Rainwater Drainage Network Z	3	11-Jan-26	14-Jan-26	04-Mar-26 A	18-Oct-26	$21,227.79	$4,245.56	100%
MOD-RWN-	Compact and shape terrain Gully Outfall to Swales for Rainwater Drainage Network Zone	2	14-Jan-26	17-Jan-26	18-Oct-26	20-Oct-26	$14,151.86	$14,151.86	100%
Riprap Works & Protection		18	28-Dec-25	18-Jan-26	15-Oct-26	05-Nov-26	$35,379.65	$35,379.65	100%
MOD-RWN-	Lay filter fabric/membrane for Rainwater Drainage Network Zone 3	3	28-Dec-25	31-Dec-25	15-Oct-26	19-Oct-26	$3,537.97	$3,537.97	100%
MOD-RWN-	Place riprap/stone layer for Rainwater Drainage Network Zone 3	10	31-Dec-25	12-Jan-26	19-Oct-26	31-Oct-26	$19,458.81	$19,458.81	100%
MOD-RWN-	Compact edges for Rainwater Drainage Network Zone 3	3	12-Jan-26	15-Jan-26	31-Oct-26	03-Nov-26	$7,075.93	$7,075.93	100%
MOD-RWN-	Ensure hydraulic flow direction for Rainwater Drainage Network Zone 3	2	15-Jan-26	18-Jan-26	03-Nov-26	05-Nov-26	$5,306.95	$5,306.95	100%
Backfilling & Bedding		181	02-Nov-25	18-Jan-26	17-Mar-26 A	26-Oct-26	2,298,195.3	$270,088.93	100%
Backfilling Materials (Type A– 201–700mm Pipes)		142	02-Nov-25	05-Jan-26	17-Mar-26 A	04-Oct-26	1,533,378.5	$44,467.98	100%
MOD-RWN-	Place granular bedding under pipe for Rainwater Drainage Network Zone 3	6	02-Nov-25	09-Nov-25	17-Mar-26 A	03-Oct-26	$153,337.85	$3,066.76	100%
MOD-RWN-	Lay and align pipe for Rainwater Drainage Network Zone 3	21	09-Nov-25	03-Dec-25	21-Mar-26 A	03-Oct-26	$690,020.34	$20,700.61	100%
MOD-RWN-	Backfill up to spring line for Rainwater Drainage Network Zone 3	13	03-Dec-25	18-Dec-25	25-Mar-26 A	04-Oct-26	$306,675.71	$9,200.27	100%
MOD-RWN-	Compact layer-wise for Rainwater Drainage Network Zone 3	9	18-Dec-25	29-Dec-25	01-Jul-26 A	04-Oct-26	$230,006.78	$6,900.20	100%
MOD-RWN-	Final fill to subgrade level for Rainwater Drainage Network Zone 3	6	29-Dec-25	05-Jan-26	01-Aug-26 A	04-Oct-26	$153,337.85	$4,600.14	100%
Gravel Bedding & Filter Cloth for uPVC Drain Pipes		136	15-Nov-25	18-Jan-26	21-Mar-26 A	26-Oct-26	$764,816.78	$225,620.95	100%
MOD-RWN-	Line trench with filter cloth for Rainwater Drainage Network Zone 3	10	15-Nov-25	26-Nov-25	21-Mar-26 A	03-Oct-26	$76,481.68	$7,648.17	100%
MOD-RWN-	Place and compact gravel bedding for Rainwater Drainage Network Zone 3	6	26-Nov-25	03-Dec-25	23-Mar-26 A	04-Oct-26	$152,963.36	$15,296.34	100%
MOD-RWN-	Lay pipe within gravel zone for Rainwater Drainage Network Zone 3	21	03-Dec-25	28-Dec-25	29-Mar-26 A	06-Oct-26	$344,167.55	$34,416.76	100%
MOD-RWN-	Wrap filter cloth above pipe for Rainwater Drainage Network Zone 3	6	28-Dec-25	04-Jan-26	01-Jul-26 A	12-Oct-26	$114,722.52	$91,778.01	100%

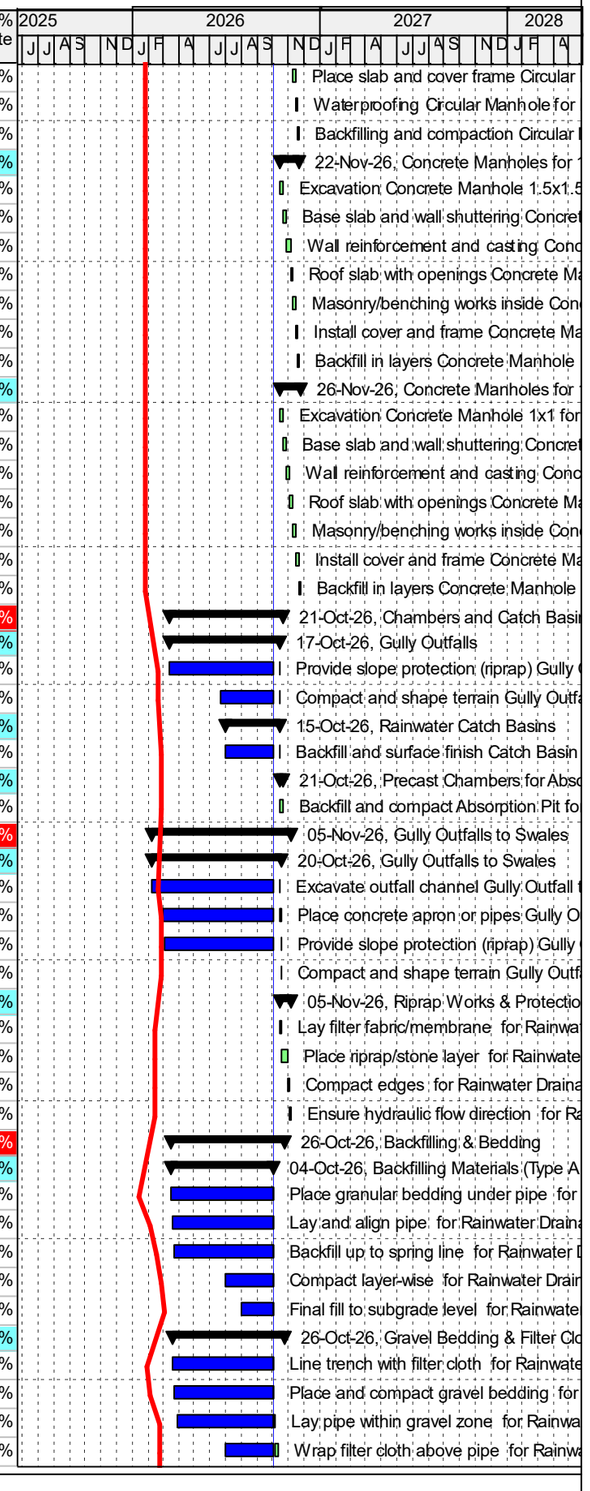


Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary

TASK filter: Schedule %.

© Oracle Corporation

Development of Phase One – Part Two – Third Industrial


Activity ID	Activity Name	Original Duration	BL Project Start	BL Project Finish	Start	Finish	Budgeted Total Cost	Remaining Total Cost	Schedule % Complete
MOD-RWN-	Final fill and trench restoration for Rainwater Drainage Network Zone 3	12	04-Jan-26	18-Jan-26	12-Oct-26	26-Oct-26	$76,481.68	$76,481.68	100%
Deep Basin for Groundwater Collection (2.5–3.0m)		146	18-Nov-25	18-Jan-26	09-Feb-26 A	26-Oct-26	4,876,369.9	$1,289,671.51	100%
MOD-RWN-DB	Base and side wall construction (cast-in-situ or precast) for Rainwater Drainage Network	10	18-Nov-25	30-Nov-25	09-Feb-26 A	04-Oct-26	2,566,510.4	$256,651.05	100%
MOD-RWN-DB	Pipe connections for inflow for Rainwater Drainage Network Zone 3	12	30-Nov-25	14-Dec-25	16-Feb-26 A	06-Oct-26	$513,302.09	$76,995.31	100%
MOD-RWN-DB	Cover slab and access shaft for Rainwater Drainage Network Zone 3	13	14-Dec-25	29-Dec-25	24-Feb-26 A	10-Oct-26	$769,953.14	$153,990.63	100%
MOD-RWN-DB	Waterproofing & sealant for Rainwater Drainage Network Zone 3	10	29-Dec-25	10-Jan-26	04-Jul-26 A	18-Oct-26	$898,278.67	$673,709.00	100%
MOD-RWN-DB	Backfill in controlled layers for Rainwater Drainage Network Zone 3	7	10-Jan-26	18-Jan-26	18-Oct-26	26-Oct-26	$128,325.52	$128,325.52	100%
Potable Water Network Zone 3		331	19-Oct-25	18-Jan-26	13-Oct-25 A	22-Dec-26	I2,014,214.8	$6,626,947.80	100%
Pipe Installation Works		72	09-Nov-25	14-Dec-25	13-Jan-26 A	13-Oct-26	$801,892.90	$330,780.82	100%
MOD-PWN-PI-	Lean Concrete / Pipe Bedding Preparation for Potable Water Network Zone 3	4	09-Nov-25	12-Nov-25	13-Jan-26 A	04-Oct-26	$50,118.31	$15,035.49	100%
MOD-PWN-PI-	HDPE Pipe Laying (200 mm to 710 mm) for Potable Water Network Zone 3	10	13-Nov-25	03-Dec-25	16-Jan-26 A	08-Oct-26	$451,064.76	$180,425.90	100%
MOD-PWN-PI-	Test (Pressure-slope) for Potable Water Network Zone 3	3	04-Dec-25	06-Dec-25	01-Feb-26 A	09-Oct-26	$100,236.61	$45,106.48	100%
MOD-PWN-PI-	Coating / Wrapping for Potable Water Network Zone 3	5	07-Dec-25	11-Dec-25	09-Feb-26 A	11-Oct-26	$100,236.61	$45,106.48	100%
MOD-PWN-PI-	Backfilling & Warning Tape for Potable Water Network Zone 3	3	12-Dec-25	14-Dec-25	23-Feb-26 A	13-Oct-26	$100,236.61	$45,106.48	100%
Valve Installation & Chambers		111	09-Nov-25	18-Jan-26	02-Jun-26 A	27-Oct-26	$316,303.42	$71,041.75	100%
MOD-PWN-VC	Valve Chamber Excavation for Potable Water Network Zone 3	10	09-Nov-25	19-Nov-25	20-Jun-26 A	03-Oct-26	$79,075.86	$7,907.59	100%
MOD-PWN-VC	RC Slab, Walls, or Precast Chambers for Potable Water Network Zone 3	7	20-Nov-25	27-Nov-25	21-Jun-26 A	04-Oct-26	$63,260.68	$6,326.07	100%
MOD-PWN-VC	Fixing Covers, Gratings, Frames for Potable Water Network Zone 3	14	27-Dec-25	11-Jan-26	04-Oct-26	20-Oct-26	$31,630.34	$31,630.34	100%
MOD-PWN-VC	Tagging & Painting for Potable Water Network Zone 3	6	12-Jan-26	18-Jan-26	20-Oct-26	27-Oct-26	$15,815.17	$15,815.17	100%
MOD-PWN-VC	Gate Valves (225–710 mm) for Potable Water Network Zone 3	12	07-Dec-25	20-Dec-25	27-Jun-26 A	04-Oct-26	$47,445.51	$4,744.55	100%
MOD-PWN-VC	Butterfly Valves (355, 500, 630 mm) for Potable Water Network Zone 3	16	07-Dec-25	24-Dec-25	02-Jun-26 A	04-Oct-26	$37,956.41	$3,795.64	100%
MOD-PWN-VC	3-exit (2 x 2.5-inch and 1 x 4-inch) dry vacuum cylinder detachable fire nozzle for Potabl	17	07-Dec-25	25-Dec-25	15-Jun-26 A	03-Oct-26	$41,119.45	$822.39	100%
Flow Meter Installation		76	20-Nov-25	11-Jan-26	12-Aug-26 A	23-Nov-26	$61,536.16	$42,152.27	100%
MOD-PWN-FM	Chamber Excavation (280 mm, 300 mm, 500 mm, 800 mm) for Potable Water Network	8	20-Nov-25	29-Nov-25	12-Aug-26 A	05-Oct-26	$18,460.85	$3,138.34	100%
MOD-PWN-FM	RC or Precast Chamber Construction for Potable Water Network Zone 3	8	30-Nov-25	08-Dec-25	05-Sep-26 A	10-Oct-26	$9,230.42	$5,169.04	100%
MOD-PWN-FM	Flowmeter Installation & Pipe Integration for Potable Water Network Zone 3	10	18-Dec-25	29-Dec-25	29-Oct-26	10-Nov-26	$21,537.66	$21,537.66	100%
MOD-PWN-FM	Wiring/Cabling if applicable for Potable Water Network Zone 3	8	30-Dec-25	07-Jan-26	10-Nov-26	19-Nov-26	$9,230.42	$9,230.42	100%
MOD-PWN-FM	Calibration & Commissioning for Potable Water Network Zone 3	3	08-Jan-26	11-Jan-26	19-Nov-26	23-Nov-26	$3,076.81	$3,076.81	100%
Washout & Air Valve Chambers		38	16-Nov-25	03-Jan-26	03-Aug-26 A	12-Oct-26	$265,589.06	$65,772.07	100%
MOD-PWN-W/	Washout (Valve + Outlet) Installation for Potable Water Network Zone 3	8	08-Dec-25	16-Dec-25	16-Aug-26 A	07-Oct-26	$64,769.25	$12,953.85	100%
MOD-PWN-W/	Air Valve Rooms (Valve + Outlet) Installation for Potable Water Network Zone 3	6	22-Dec-25	28-Dec-25	16-Aug-26 A	10-Oct-26	$45,075.10	$9,015.02	100%
MOD-PWN-W/	Covers, Ladders & Tags for Potable Water Network Zone 3	3	29-Dec-25	31-Dec-25	15-Sep-26 A	10-Oct-26	$19,468.09	$3,893.62	100%
MOD-PWN-W/	Backfilling & Final Finishing for Potable Water Network Zone 3	2	01-Jan-26	03-Jan-26	10-Oct-26	12-Oct-26	$19,468.09	$19,468.09	100%
MOD-PWN-W/	RC Blinding + Base + Walls for Potable Water Network Zone 3	4	16-Nov-25	19-Nov-25	03-Aug-26 A	03-Oct-26	$29,202.13	$2,920.21	100%
MOD-PWN-W/	Pipe Work for Potable Water Network Zone 3	15	20-Nov-25	07-Dec-25	08-Aug-26 A	06-Oct-26	$87,606.40	$17,521.28	100%
Pumping Station (Structure & Civil Works)		66	19-Oct-25	04-Jan-26	03-Oct-26	17-Dec-26	$473,145.06	$473,145.06	100%
MOD-PWN-PS	Pump Base Pads + Grouting for Potable Water Network Zone 3	13	30-Nov-25	15-Dec-25	14-Nov-26	28-Nov-26	$78,857.51	$78,857.51	100%
MOD-PWN-PS	Backfilling & External Finishes for Potable Water Network Zone 3	17	15-Dec-25	04-Jan-26	29-Nov-26	17-Dec-26	$78,857.51	$78,857.51	100%
MOD-PWN-PS	Excavation & Blinding for Potable Water Network Zone 3	10	19-Oct-25	30-Oct-25	03-Oct-26	13-Oct-26	$78,857.51	$78,857.51	100%
MOD-PWN-PS	Reinforced Concrete/GRP Shell Construction for Potable Water Network Zone 3	8	30-Oct-25	09-Nov-25	14-Oct-26	22-Oct-26	$78,857.51	$78,857.51	100%
MOD-PWN-PS	Access Ladders, Tight Cover, Surface Guttering for Potable Water Network Zone 3	5	09-Nov-25	15-Nov-25	24-Oct-26	28-Oct-26	$78,857.51	$78,857.51	100%
MOD-PWN-PS	Internal piping & embedded sleeves for Potable Water Network Zone 3	13	15-Nov-25	30-Nov-25	29-Oct-26	12-Nov-26	$78,857.51	$78,857.51	100%
Pump Station Building		31	30-Nov-25	05-Jan-26	14-Nov-26	19-Dec-26	$183,637.93	$183,637.93	100%
MOD-PWN-PB	Structure Construction (as per architectural drawings) for Potable Water Network Zone 3	13	30-Nov-25	15-Dec-25	14-Nov-26	28-Nov-26	$78,857.51	$78,857.51	100%
MOD-PWN-PB	5-ton Hoist Installation for Potable Water Network Zone 3	5	15-Dec-25	21-Dec-25	29-Nov-26	03-Dec-26	$25,922.91	$25,922.91	100%
MOD-PWN-PB	Finishes, Doors, Ventilation for Potable Water Network Zone 3	13	21-Dec-25	05-Jan-26	05-Dec-26	19-Dec-26	$78,857.51	$78,857.51	100%
Pumping Equipment & Fire Systems		28	17-Dec-25	18-Jan-26	14-Nov-26	15-Dec-26	$946,290.12	$946,290.12	100%
MOD-PWN-PE	Diesel Fire Water Pump (64 L/s @ 60 m) for Potable Water Network Zone 3	6	03-Jan-26	08-Jan-26	30-Nov-26	06-Dec-26	$86,409.76	$86,409.76	100%
MOD-PWN-PE	Electric Jockey Pump for Potable Water Network Zone 3	6	03-Jan-26	08-Jan-26	30-Nov-26	06-Dec-26	$48,005.39	$48,005.39	100%

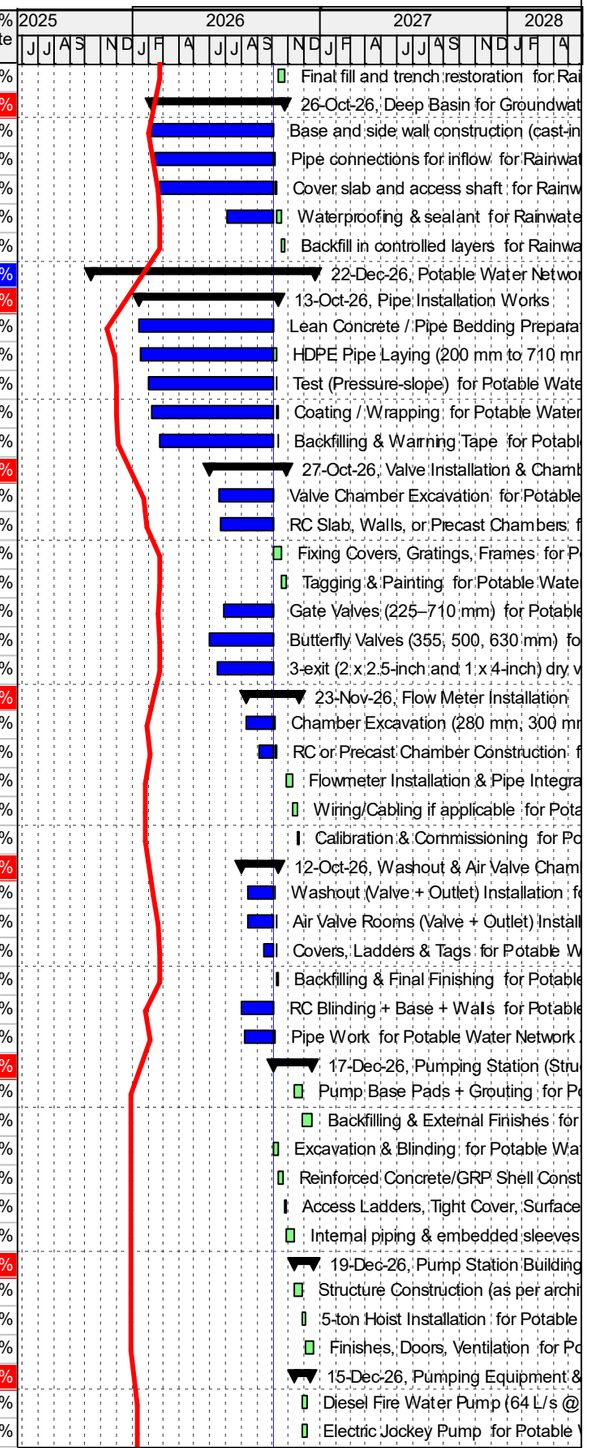

© Oracle Corporation

Development of Phase One – Part Two – Third Industrial

Activity ID	Activity Name	Original Duration	BL Project Start	BL Project Finish	Start	Finish	Budgeted Total Cost	Remaining Total Cost	Schedule % Complete
MOD-PWN-PE	Submersible Fire Pumps (2 pcs, 10 L/s @ 10 m) for Potable Water Network Zone 3	4	03-Jan-26	06-Jan-26	30-Nov-26	03-Dec-26	$36,483.86	$36,483.86	100%
MOD-PWN-PE	Pipework connections within Pump Room for Potable Water Network Zone 3	5	07-Jan-26	12-Jan-26	05-Dec-26	09-Dec-26	$78,857.51	$78,857.51	100%
MOD-PWN-PE	MCC & DB panel installation for Potable Water Network Zone 3	2	13-Jan-26	14-Jan-26	10-Dec-26	12-Dec-26	$78,857.51	$78,857.51	100%
MOD-PWN-PE	Flow meter on 800mm pipe including flow meter chamber and 2-2.5m depth for Potable	3	15-Jan-26	18-Jan-26	13-Dec-26	15-Dec-26	$82,788.23	$82,788.23	100%
MOD-PWN-PE	Main Pumps (250 kW, 295 L/s @ 60 m head) for Potable Water Network Zone 3	14	17-Dec-25	01-Jan-26	14-Nov-26	29-Nov-26	$438,877.07	$438,877.07	100%
MOD-PWN-PE	Electric Fire Water Pump (64 L/s @ 60 m) for Potable Water Network Zone 3	8	03-Jan-26	11-Jan-26	30-Nov-26	08-Dec-26	$96,010.78	$96,010.78	100%
Surge Protection		5	13-Jan-26	18-Jan-26	10-Dec-26	15-Dec-26	$28,227.66	$28,227.66	100%
MOD-PWN-SP	Surge Vessel Installation for Potable Water Network Zone 3	4	13-Jan-26	17-Jan-26	10-Dec-26	14-Dec-26	$22,582.13	$22,582.13	100%
MOD-PWN-SP	Pipe Integration as per Surge Analysis for Potable Water Network Zone 3	1	18-Jan-26	18-Jan-26	15-Dec-26	15-Dec-26	$5,645.53	$5,645.53	100%
Power & Generator System		12	03-Jan-26	15-Jan-26	30-Nov-26	13-Dec-26	2,851,518.7	$2,851,518.70	100%
MOD-PWN-PG	500 kVA Standby Generator Installation for Potable Water Network Zone 3	4	03-Jan-26	06-Jan-26	30-Nov-26	03-Dec-26	2,281,214.9	$2,281,214.96	100%
MOD-PWN-PG	Canopy, Foundation & Fuel Tank for Potable Water Network Zone 3	6	03-Jan-26	08-Jan-26	30-Nov-26	06-Dec-26	$285,151.87	$285,151.87	100%
MOD-PWN-PG	Electrical Cabling, Circuit Breakers for Potable Water Network Zone 3	4	10-Jan-26	13-Jan-26	07-Dec-26	10-Dec-26	$142,575.94	$142,575.94	100%
MOD-PWN-PG	Earthing & Commissioning for Potable Water Network Zone 3	2	14-Jan-26	15-Jan-26	12-Dec-26	13-Dec-26	$142,575.94	$142,575.94	100%
Chlorination System		14	03-Jan-26	18-Jan-26	30-Nov-26	15-Dec-26	$518,457.97	$518,457.97	100%
MOD-PWN-CS	Chlorination Device Supply & Installation for Potable Water Network Zone 3	7	03-Jan-26	10-Jan-26	30-Nov-26	07-Dec-26	$362,920.58	$362,920.58	100%
MOD-PWN-CS	Connections to Main Line or Disinfection Chamber for Potable Water Network Zone 3	4	11-Jan-26	14-Jan-26	08-Dec-26	12-Dec-26	$103,691.59	$103,691.59	100%
MOD-PWN-CS	Control Integration for Potable Water Network Zone 3	3	15-Jan-26	18-Jan-26	13-Dec-26	15-Dec-26	$51,845.80	$51,845.80	100%
Water Storage System		11	05-Jan-26	18-Jan-26	13-Oct-25 A	22-Dec-26	5,159,570.0	$1,031,914.01	100%
MOD-PWN-WS	Structural tanks for supply or pressure equalization for Potable Water Network Zone 3	11	05-Jan-26	18-Jan-26	13-Oct-25 A	22-Dec-26	5,159,570.0	$1,031,914.01	100%
Street Lighting		220	22-Dec-25	18-Jan-26	13-Dec-25 A	07-Dec-26	$408,045.82	$84,009.43	100%
MOD-PWN-SL-	Conduits, Cabling, Backfilling for Potable Water Network Zone 3	12	22-Dec-25	05-Jan-26	15-Dec-25 A	30-Nov-26	$72,008.09	$7,200.81	100%
MOD-PWN-SL-	Pole & Fixture Installation for Potable Water Network Zone 3	16	24-Dec-25	11-Jan-26	13-Dec-25 A	30-Nov-26	$288,032.34	$28,803.23	100%
MOD-PWN-SL-	Connection to Main Supply for Potable Water Network Zone 3	6	12-Jan-26	18-Jan-26	30-Nov-26	07-Dec-26	$24,002.70	$24,002.70	100%
MOD-PWN-SL-	Testing & Lighting Commissioning for Potable Water Network Zone 3	6	12-Jan-26	18-Jan-26	30-Nov-26	07-Dec-26	$24,002.70	$24,002.70	100%
Irrigation Network Zone 3		211	19-Oct-25	11-Jan-26	01-Apr-26 A	15-Nov-26	$655,124.78	$114,230.69	100%
Excavation, Pipe Laying & Backfilling		158	19-Oct-25	14-Dec-25	01-Apr-26 A	09-Oct-26	$546,284.50	$85,220.38	100%
MOD-IRN-EB-1	Trench Excavation for Irrigation Network Zone 3	21	19-Oct-25	08-Nov-25	01-Apr-26 A	05-Oct-26	$109,256.90	$10,925.69	100%
MOD-IRN-EB-1	Lean Concrete / Pipe Bedding with Type B Material for Irrigation Network Zone 3	9	09-Nov-25	17-Nov-25	04-Apr-26 A	05-Oct-26	$27,314.22	$2,731.42	100%
MOD-IRN-EB-1	HDPE Pipe Laying (125 mm to 630 mm) for Irrigation Network Zone 3	21	18-Nov-25	08-Dec-25	07-Apr-26 A	08-Oct-26	$245,828.02	$24,582.80	100%
MOD-IRN-EB-1	Test (Pressure-slope) for Irrigation Network Zone 3	2	09-Dec-25	10-Dec-25	01-May-26 A	08-Oct-26	$54,628.45	$9,833.12	100%
MOD-IRN-EB-1	Coating / Wrapping for Irrigation Network Zone 3	2	11-Dec-25	12-Dec-25	01-Jun-26 A	08-Oct-26	$54,628.45	$9,833.12	100%
MOD-IRN-EB-1	Backfilling & Warning Tape for Irrigation Network Zone 3	2	13-Dec-25	14-Dec-25	13-Jul-26 A	09-Oct-26	$54,628.45	$27,314.22	100%
Valves and Appurtenances		22	11-Dec-25	28-Dec-25	20-Jun-26 A	06-Oct-26	$24,177.05	$5,280.60	100%
MOD-IRN-VA-6	Supply & Installation of Valves (Butterfly Valve) for Irrigation Network Zone 3	8	11-Dec-25	20-Dec-25	20-Jun-26 A	04-Oct-26	$17,817.16	$3,563.43	100%
MOD-IRN-VA-7	Installation of Flanges, Bolts, Collars, Nuts for Irrigation Network Zone 3	3	21-Dec-25	23-Dec-25	21-Jun-26 A	05-Oct-26	$2,543.95	$508.79	100%
MOD-IRN-VA-8	Valve Pressure Testing for Irrigation Network Zone 3	2	24-Dec-25	25-Dec-25	06-Jul-26 A	05-Oct-26	$1,589.97	$317.99	100%
MOD-IRN-VA-9	Support Brackets/Anchor Blocks for Irrigation Network Zone 3	2	27-Dec-25	28-Dec-25	07-Jul-26 A	06-Oct-26	$2,225.96	$890.38	100%
Valve Rooms		2	31-Dec-25	01-Jan-26	11-Jul-26 A	03-Oct-26	$3,007.40	$451.11	100%
MOD-IRN-VR-1	Backfilling and Finishing Valve Chamber for Irrigation Network Zone 3	2	31-Dec-25	01-Jan-26	11-Jul-26 A	03-Oct-26	$3,007.40	$451.11	100%
Washout Chambers		24	25-Dec-25	08-Jan-26	16-Jun-26 A	04-Oct-26	$38,668.73	$3,866.87	100%
MOD-IRN-WC-	Manhole Frame, Cover & Ladder Fixing Washout Chamber for Irrigation Network Zone 3	3	31-Dec-25	03-Jan-26	22-Jun-26 A	03-Oct-26	$10,546.02	$1,054.60	100%
MOD-IRN-WC-	Backfilling & Reinstatement Washout Chamber for Irrigation Network Zone 3	5	04-Jan-26	08-Jan-26	06-Jul-26 A	04-Oct-26	$3,515.34	$351.53	100%
MOD-IRN-WC-	Washout Valve & Pipe Connection Washout Chamber for Irrigation Network Zone 3	5	25-Dec-25	30-Dec-25	16-Jun-26 A	03-Oct-26	$24,607.37	$2,460.74	100%
Air Valve Chambers		2	05-Jan-26	06-Jan-26	23-Jun-26 A	03-Oct-26	$7,117.25	$355.86	100%
MOD-IRN-AC-9	Cover Fixing & Finishing Air Valve Chamber for Irrigation Network Zone 3	2	05-Jan-26	06-Jan-26	23-Jun-26 A	03-Oct-26	$7,117.25	$355.86	100%
Flow Meter Chambers		136	13-Dec-25	11-Jan-26	27-May-26 A	15-Nov-26	$35,869.85	$19,055.86	100%
MOD-IRN-FC-1	Testing & Calibration Flow Meter Chamber for Irrigation Network Zone 3	6	31-Dec-25	06-Jan-26	03-Nov-26	10-Nov-26	$6,725.60	$6,725.60	100%
MOD-IRN-FC-1	Cover and Access Arrangement Flow Meter Chamber for Irrigation Network Zone 3	4	07-Jan-26	11-Jan-26	10-Nov-26	15-Nov-26	$2,241.87	$2,241.87	100%
MOD-IRN-FC-7	RCC Base & Wall Construction Flow Meter Chamber for Irrigation Network Zone 3	4	13-Dec-25	16-Dec-25	27-May-26 A	03-Oct-26	$4,483.73	$1,120.93	100%

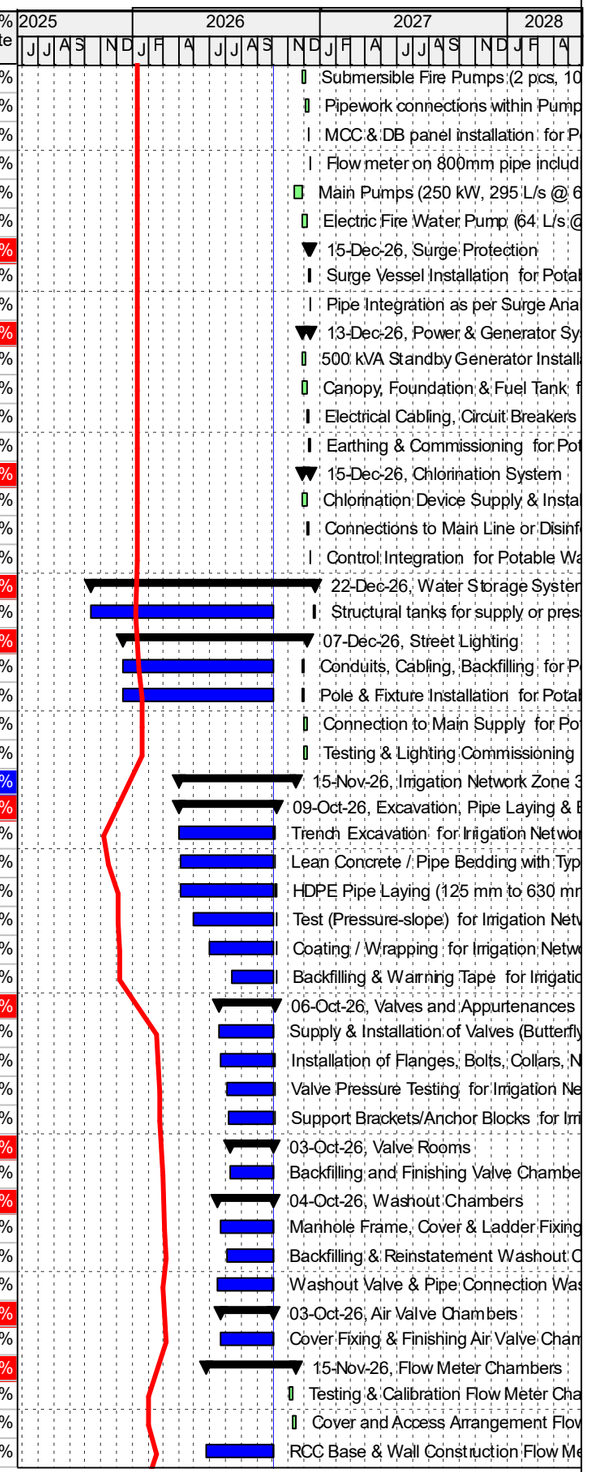


Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary

TASK filter: Schedule %.

© Oracle Corporation

Development of Phase One – Part Two – Third Industrial

Activity ID	Activity Name	Original Duration	BL Project Start	BL Project Finish	Start	Finish	Budgeted Total Cost	Remaining Total Cost	Schedule % Complete
MOD-IRN-FC-8	Flow Meter Installation (280, 300, 500 mm) Flow Meter Chamber for Irrigation Network Z	6	18-Dec-25	24-Dec-25	01-Jul-26 A	01-Nov-26	$15,693.06	$6,277.22	100%
MOD-IRN-FC-9	Integration with Pipework Flow Meter Chamber for Irrigation Network Zone 3	5	25-Dec-25	30-Dec-25	02-Jul-26 A	03-Nov-26	$6,725.60	$2,690.24	100%
Rainwater Collection Ponds Zone 3		267	22-Jan-26	17-Aug-26	04-Oct-25 A	20-Mar-27	16,824,279.(	$2,614,847.50	100%
Excavation for Rainwater Drainage Pond		223	22-Jan-26	14-Mar-26	04-Oct-25 A	09-Jan-27	$380,829.23	$68,864.97	100%
Deep excavation, backfill, disposal for pond formation		223	22-Jan-26	14-Mar-26	04-Oct-25 A	09-Jan-27	$380,829.23	$68,864.97	100%
MOD-RCP-E	Place warning tapes for Rainwater Collection Ponds Zone 3	6	11-Feb-26	19-Feb-26	01-Jul-26 A	04-Jan-27	$29,598.13	$5,919.63	100%
MOD-RCP-E	Dispose of rock/materials to approved dump area for Rainwater Collection Ponds Zone :	7	19-Feb-26	05-Mar-26	10-Aug-26 A	06-Jan-27	$98,660.42	$19,732.08	100%
MOD-RCP-E	Backfill selected areas as per design for Rainwater Collection Ponds Zone 3	2	07-Mar-26	10-Mar-26	01-Sep-26 A	06-Jan-27	$7,892.83	$1,578.57	100%
MOD-RCP-E	Final trimming and profiling for Rainwater Collection Ponds Zone 3	2	10-Mar-26	14-Mar-26	06-Jan-27	09-Jan-27	$5,919.63	$5,919.63	100%
MOD-RCP-E	Excavate in layers to final depth for Rainwater Collection Ponds Zone 3	12	22-Jan-26	04-Feb-26	04-Oct-25 A	02-Jan-27	$120,365.71	$12,036.57	100%
MOD-RCP-E	Dewater during excavation for Rainwater Collection Ponds Zone 3	5	05-Feb-26	10-Feb-26	01-Mar-26 A	03-Jan-27	$118,392.51	$23,678.50	100%
General Site Preparation		39	16-Mar-26	10-May-26	12-Oct-25 A	05-Jan-27	14,165,976.4	$1,416,597.64	100%
MOD-RCP-GS-	Earthwork excavation (other than topsoil or rock) - Zone 3 (3 Ponds) for Rainwater Colle	21	16-Mar-26	15-Apr-26	12-Oct-25 A	03-Jan-27	7,689,673.8	$768,967.39	100%
MOD-RCP-GS-	Transport and disposal to approved locations - Zone 3 (3 Ponds) for Rainwater Collectio	21	15-Apr-26	10-May-26	06-Dec-25 A	05-Jan-27	6,476,302.5	$647,630.26	100%
Backfilling Works		174	10-May-26	29-Jul-26	18-Nov-25 A	21-Jan-27	$844,533.44	$162,150.42	100%
MOD-RCP-BW	Select material from excavation or import approved material for Rainwater Collection Po	15	10-May-26	01-Jun-26	11-Dec-25 A	07-Jan-27	$168,906.69	$16,890.67	100%
MOD-RCP-BW	Place in layers not exceeding 300mm for Rainwater Collection Ponds Zone 3	21	01-Jun-26	25-Jun-26	29-Nov-25 A	10-Jan-27	$295,586.71	$35,470.40	100%
MOD-RCP-BW	Compact each layer to required density for Rainwater Collection Ponds Zone 3	20	25-Jun-26	19-Jul-26	18-Nov-25 A	14-Jan-27	$211,133.36	$42,226.67	100%
MOD-RCP-BW	Conduct field density tests for Rainwater Collection Ponds Zone 3	4	19-Jul-26	23-Jul-26	01-Aug-26 A	16-Jan-27	$126,680.02	$25,336.00	100%
MOD-RCP-BW	Final leveling and approval for Rainwater Collection Ponds Zone 3	5	23-Jul-26	29-Jul-26	16-Jan-27	21-Jan-27	$42,226.67	$42,226.67	100%
Geotextile & Bedding		206	01-Jun-26	17-Aug-26	12-Jan-26 A	20-Mar-27	1,432,939.9	$967,234.46	100%
Installation of geotextile lining and coarse sand bedding		206	01-Jun-26	17-Aug-26	12-Jan-26 A	20-Mar-27	1,432,939.9	$967,234.46	100%
MOD-RCP-(	Trim subgrade to required level for Rainwater Collection Ponds Zone 3	7	01-Jun-26	09-Jun-26	12-Jan-26 A	09-Jan-27	$143,293.99	$28,658.80	100%
MOD-RCP-(	Lay HDPE geotextile membrane over compacted soil for Rainwater Collection Ponds Zo	21	09-Jun-26	04-Jul-26	29-Jan-26 A	16-Jan-27	$501,528.98	$150,458.69	100%
MOD-RCP-(	Place 500mm thick coarse sand bedding for Rainwater Collection Ponds Zone 3	21	04-Jul-26	28-Jul-26	17-Jan-27	11-Feb-27	$429,881.98	$429,881.98	100%
MOD-RCP-(	Compact and level bedding for Rainwater Collection Ponds Zone 3	17	28-Jul-26	17-Aug-26	13-Feb-27	20-Mar-27	$358,234.99	$358,234.99	100%
Road Crossing Zone 3		253	12-Feb-26	07-Oct-26	01-Apr-26 A	24-Jun-27	$732,112.24	$521,614.41	99.07%
uPVC Road Crossing Pipes		162	12-Feb-26	22-Jun-26	01-Apr-26 A	24-Feb-27	$511,209.02	$300,711.19	100%
Installation of uPVC pipes of various diameters crossing roadways		162	12-Feb-26	22-Jun-26	01-Apr-26 A	24-Feb-27	$511,209.02	$300,711.19	100%
MOD-ROC-F	Excavation across road width to required depth for Road Crossing Zone 3	10	12-Feb-26	26-Mar-26	09-Jun-26 A	05-Jan-27	$90,213.36	$36,085.34	100%
MOD-ROC-F	Preparation of trench base with compacted bedding for Road Crossing Zone 3	10	26-Mar-26	13-Apr-26	01-Apr-26 A	10-Jan-27	$60,142.24	$24,056.90	100%
MOD-ROC-F	Laying of uPVC pipe (300mm, 315mm, 400mm, 600mm dia) for Road Crossing Zone 3	10	13-Apr-26	07-May-26	01-May-26 A	16-Jan-27	$240,568.95	$120,284.48	100%
MOD-ROC-F	Placement of supports and protection around the pipe for Road Crossing Zone 3	5	07-May-26	19-May-26	16-Jan-27	21-Jan-27	$60,142.24	$60,142.24	100%
MOD-ROC-F	Testing of installed pipeline for Road Crossing Zone 3	6	19-May-26	26-May-26	21-Jan-27	28-Jan-27	$15,035.56	$15,035.56	100%
MOD-ROC-F	Backfilling and compaction in layers for Road Crossing Zone 3	10	26-May-26	15-Jun-26	28-Jan-27	11-Feb-27	$30,071.12	$30,071.12	100%
MOD-ROC-F	Reinstatement of road surface for Road Crossing Zone 3	6	15-Jun-26	22-Jun-26	11-Feb-27	24-Feb-27	$15,035.56	$15,035.56	100%
GRP Road Crossing Pipes		91	22-Jun-26	07-Oct-26	24-Feb-27	24-Jun-27	$220,903.22	$220,903.22	96.92%
Installation of GRP pipes (800mm–1000mm dia) for road crossings		91	22-Jun-26	07-Oct-26	24-Feb-27	24-Jun-27	$220,903.22	$220,903.22	96.92%
MOD-ROC-(	Set out location and coordinate with road authority for Road Crossing Zone 3	5	22-Jun-26	28-Jun-26	24-Feb-27	06-Mar-27	$11,328.37	$11,328.37	100%
MOD-ROC-(	Excavate trench across road at designed depth for Road Crossing Zone 3	12	28-Jun-26	12-Jul-26	06-Mar-27	25-Mar-27	$22,656.74	$22,656.74	100%
MOD-ROC-(	Lay compacted granular bedding for Road Crossing Zone 3	16	12-Jul-26	30-Jul-26	27-Mar-27	13-Apr-27	$33,985.11	$33,985.11	100%
MOD-ROC-(	Install GRP pipe (800mm & 1000mm dia) for Road Crossing Zone 3	21	30-Jul-26	24-Aug-26	14-Apr-27	08-May-27	$90,626.96	$90,626.96	100%
MOD-ROC-(	Provide structural supports and closure at both ends for Road Crossing Zone 3	9	24-Aug-26	03-Sep-26	09-May-27	23-May-27	$22,656.74	$22,656.74	100%
MOD-ROC-(	Perform leak testing as per specifications for Road Crossing Zone 3	5	03-Sep-26	09-Sep-26	24-May-27	29-May-27	$5,664.19	$5,664.19	100%
MOD-ROC-(	Backfill and compact in layers for Road Crossing Zone 3	15	09-Sep-26	28-Sep-26	30-May-27	15-Jun-27	$22,656.74	$22,656.74	100%
MOD-ROC-(	Reinstate road surface (asphalt/concrete) for Road Crossing Zone 3	8	28-Sep-26	07-Oct-26	16-Jun-27	24-Jun-27	$11,328.37	$11,328.37	40%
Zone 2		579	19-Oct-25	07-Oct-26	17-Nov-25 A	27-Jul-27	14,514,678.3	$6,067,669.05	99.91%
Sewerage Network Zone 2		319	19-Oct-25	04-Mar-26	11-Jan-26 A	08-Dec-26	2,068,009.6	$880,516.49	100%
Pipework: Supply, Installation, and Testing		307	19-Oct-25	03-Feb-26	11-Jan-26 A	25-Nov-26	$208,367.13	$102,308.26	100%
HDPE Pressure Pipes Installation (250mm–630mm)		307	19-Oct-25	03-Feb-26	11-Jan-26 A	25-Nov-26	$208,367.13	$102,308.26	100%

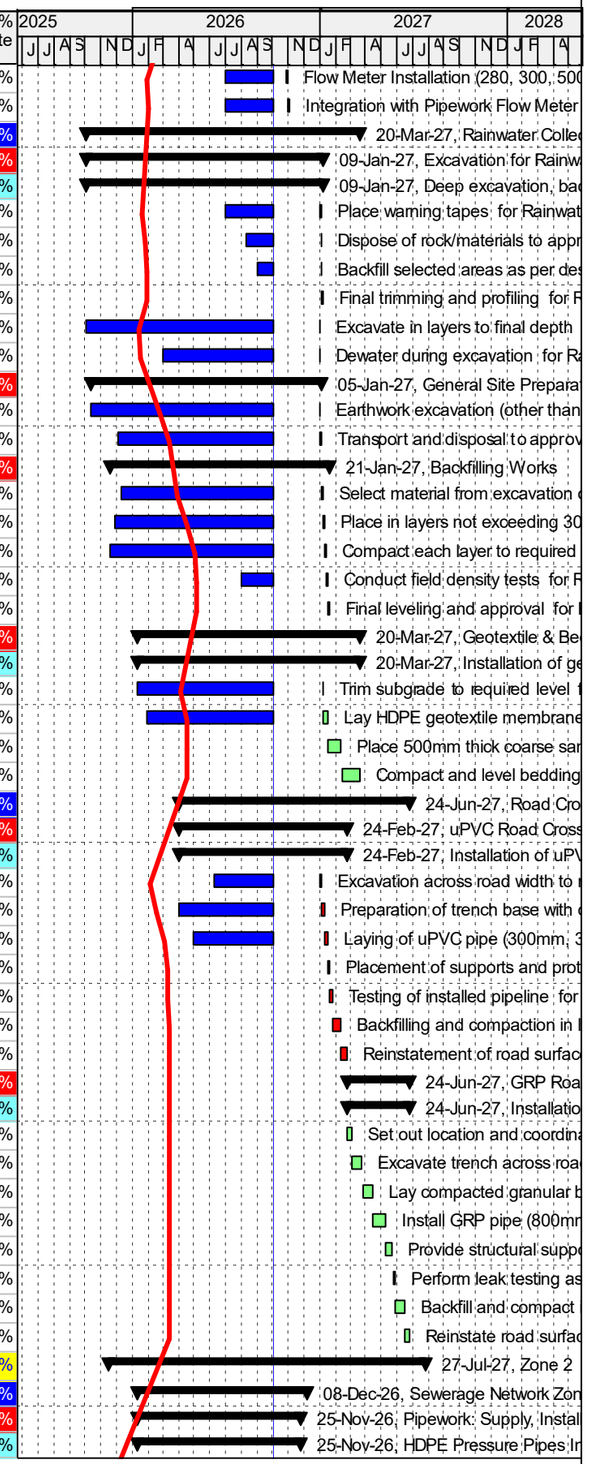


Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary

TASK filter: Schedule %.

© Oracle Corporation

Development of Phase One – Part Two – Third Industrial

Activity ID	Activity Name	Original Duration	BL Project Start	BL Project Finish	Start	Finish	Budgeted Total Cost	Remaining Total Cost	Schedule % Complete
MOD-SWN-	HDPE Pressure Pipes Installation (250mm–630mm) HDPE for Sewerage Network Zone :	21	30-Nov-25	20-Dec-25	09-Feb-26 A	26-Oct-26	$93,765.21	$46,882.61	100%
MOD-SWN-	Backfilling & Warrning Tape HDPE for Sewerage Network Zone 2	15	20-Jan-26	03-Feb-26	11-Nov-26	25-Nov-26	$20,836.71	$20,836.71	100%
MOD-SWN-	Excavation and Trenching HDPE for Sewerage Network Zone 2	21	19-Oct-25	08-Nov-25	11-Jan-26 A	07-Oct-26	$41,673.43	$8,334.69	100%
MOD-SWN-	Lean Concrete / Bedding HDPE for Sewerage Network Zone 2	21	09-Nov-25	29-Nov-25	15-Jan-26 A	15-Oct-26	$10,418.36	$4,167.34	100%
MOD-SWN-	Test (Pressure - Slope) HDPE for Sewerage Network Zone 2	15	21-Dec-25	04-Jan-26	16-Mar-26 A	02-Nov-26	$20,836.71	$10,418.36	100%
MOD-SWN-	Coating / Wrapping HDPE for Sewerage Network Zone 2	15	05-Jan-26	19-Jan-26	21-Mar-26 A	10-Nov-26	$20,836.71	$11,668.56	100%
Fittings and Valves		27	21-Dec-25	20-Jan-26	26-Oct-26	26-Nov-26	$61,422.41	$61,422.41	100%
MOD-SWN-FV-	Gate Valves Installation for Sewerage Network Zone 2	4	28-Dec-25	31-Dec-25	02-Nov-26	07-Nov-26	$9,660.60	$9,660.60	100%
MOD-SWN-FV-	Drain Valves Installation for Sewerage Network Zone 2	4	01-Jan-26	05-Jan-26	07-Nov-26	11-Nov-26	$8,785.65	$8,785.65	100%
MOD-SWN-FV-	Air Breather & Air Release Valves Installation for Sewerage Network Zone 2	10	06-Jan-26	17-Jan-26	11-Nov-26	23-Nov-26	$23,181.49	$23,181.49	100%
MOD-SWN-FV-	Jointing & Piping Accessories Installation for Sewerage Network Zone 2	3	18-Jan-26	20-Jan-26	23-Nov-26	26-Nov-26	$6,142.24	$6,142.24	100%
MOD-SWN-FV-	Supply & Installation of HDPE Elbows for Sewerage Network Zone 2	6	21-Dec-25	27-Dec-25	26-Oct-26	02-Nov-26	$13,652.43	$13,652.43	100%
Valve & Flow Meter Chambers		148	19-Oct-25	10-Feb-26	01-Jul-26 A	08-Dec-26	$99,848.78	$63,407.36	100%
Valve Chambers Construction		127	19-Oct-25	04-Jan-26	01-Jul-26 A	17-Nov-26	$13,788.12	$8,203.93	100%
MOD-SWN-	Backfilling Valve Chamber for Sewerage Network Zone 2	15	21-Dec-25	04-Jan-26	02-Nov-26	17-Nov-26	$2,757.62	$2,757.62	100%
MOD-SWN-	Excavation Valve Chamber for Sewerage Network Zone 2	21	19-Oct-25	08-Nov-25	01-Jul-26 A	07-Oct-26	$2,068.22	$413.64	100%
MOD-SWN-	Lean Concrete / Bedding Valve Chamber for Sewerage Network Zone 2	21	09-Nov-25	29-Nov-25	14-Jul-26 A	15-Oct-26	$1,378.81	$551.52	100%
MOD-SWN-	Test Valve Chamber for Sewerage Network Zone 2	15	06-Dec-25	20-Dec-25	18-Oct-26	02-Nov-26	$1,378.81	$1,378.81	100%
MOD-SWN-	Valve Chambers Construction Valve Chamber for Sewerage Network Zone 2	6	30-Nov-25	05-Dec-25	28-Jul-26 A	18-Oct-26	$6,204.65	$3,102.33	100%
Water Drain Chambers Construction		69	19-Oct-25	23-Jan-26	28-Jul-26 A	27-Nov-26	$44,788.55	$26,649.19	100%
MOD-SWN-	Backfilling Water Drain Chamber for Sewerage Network Zone 2	15	09-Jan-26	23-Jan-26	12-Nov-26	27-Nov-26	$8,957.71	$8,957.71	100%
MOD-SWN-	Excavation Water Drain Chamber for Sewerage Network Zone 2	21	19-Oct-25	08-Nov-25	28-Jul-26 A	07-Oct-26	$6,718.28	$1,343.66	100%
MOD-SWN-	Lean Concrete / Bedding Water Drain Chamber for Sewerage Network Zone 2	21	09-Nov-25	29-Nov-25	01-Aug-26 A	15-Oct-26	$4,478.86	$1,791.54	100%
MOD-SWN-	Test Water Drain Chamber for Sewerage Network Zone 2	15	25-Dec-25	08-Jan-26	28-Oct-26	12-Nov-26	$4,478.86	$4,478.86	100%
MOD-SWN-	Water Drain Chambers Construction Water Drain Chamber for Sewerage Network Zone :	19	06-Dec-25	24-Dec-25	18-Aug-26 A	28-Oct-26	$20,154.85	$10,077.42	100%
Discharge Chambers Construction		76	19-Oct-25	05-Feb-26	14-Jul-26 A	03-Dec-26	$31,287.23	$19,867.39	100%
MOD-SWN-	Backfilling Discharge Chamber for Sewerage Network Zone 2	15	22-Jan-26	05-Feb-26	18-Nov-26	03-Dec-26	$6,257.45	$6,257.45	100%
MOD-SWN-	Excavation Discharge Chamber for Sewerage Network Zone 2	21	19-Oct-25	08-Nov-25	14-Jul-26 A	11-Oct-26	$4,693.08	$1,877.23	100%
MOD-SWN-	Lean Concrete / Bedding Discharge Chamber for Sewerage Network Zone 2	21	09-Nov-25	29-Nov-25	17-Aug-26 A	21-Oct-26	$3,128.72	$1,564.36	100%
MOD-SWN-	Test Discharge Chamber for Sewerage Network Zone 2	15	07-Jan-26	21-Jan-26	03-Nov-26	18-Nov-26	$3,128.72	$3,128.72	100%
MOD-SWN-	Discharge Chambers Construction Discharge Chamber for Sewerage Network Zone 2	13	25-Dec-25	06-Jan-26	18-Aug-26 A	03-Nov-26	$14,079.25	$7,039.63	100%
Flow Meter Chambers Construction		81	19-Oct-25	10-Feb-26	19-Aug-26 A	08-Dec-26	$9,984.88	$8,686.84	100%
MOD-SWN-	Backfilling Flow Meter Chamber for Sewerage Network Zone 2	15	27-Jan-26	10-Feb-26	23-Nov-26	08-Dec-26	$1,996.98	$1,996.98	100%
MOD-SWN-	Excavation Flow Meter Chamber for Sewerage Network Zone 2	21	19-Oct-25	08-Nov-25	19-Aug-26 A	11-Oct-26	$1,497.73	$599.09	100%
MOD-SWN-	Lean Concrete / Bedding Flow Meter Chamber for Sewerage Network Zone 2	21	09-Nov-25	29-Nov-25	26-Aug-26 A	23-Oct-26	$998.49	$599.09	100%
MOD-SWN-	Test Flow Meter Chamber for Sewerage Network Zone 2	15	12-Jan-26	26-Jan-26	08-Nov-26	23-Nov-26	$998.49	$998.49	100%
MOD-SWN-	Flow Meter Chambers Construction Flow Meter Chamber for Sewerage Network Zone 2	5	07-Jan-26	11-Jan-26	03-Nov-26	08-Nov-26	$4,493.20	$4,493.20	100%
Manholes		266	19-Oct-25	04-Mar-26	01-Feb-26 A	14-Nov-26	1,698,371.3	$653,378.46	100%
1200mm GRP Manholes with Backdrop		260	19-Oct-25	19-Jan-26	01-Feb-26 A	08-Nov-26	$845,258.26	$317,817.11	100%
MOD-SWN-	1200mm GRP Manholes with Backdrop 1.2m GRP for Sewerage Network Zone 2	21	30-Nov-25	20-Dec-25	14-Feb-26 A	09-Oct-26	$380,366.22	$45,643.95	100%
MOD-SWN-	Backfilling 1.2m GRP for Sewerage Network Zone 2	15	05-Jan-26	19-Jan-26	24-Oct-26	08-Nov-26	$169,051.65	$169,051.65	100%
MOD-SWN-	Excavation 1.2m GRP for Sewerage Network Zone 2	21	19-Oct-25	08-Nov-25	01-Feb-26 A	04-Oct-26	$126,788.74	$10,143.10	100%
MOD-SWN-	Lean Concrete / Bedding 1.2m GRP for Sewerage Network Zone 2	21	09-Nov-25	29-Nov-25	07-Feb-26 A	06-Oct-26	$84,525.83	$8,452.58	100%
MOD-SWN-	Test 1.2m GRP for Sewerage Network Zone 2	15	21-Dec-25	04-Jan-26	09-Oct-26	24-Oct-26	$84,525.83	$84,525.83	100%
1500mm GRP Manholes (Standard & Backdrop)		263	19-Oct-25	09-Feb-26	12-Feb-26 A	11-Nov-26	$800,529.72	$315,808.97	100%
MOD-SWN-	1500mm GRP Manholes (Standard & Backdrop) 1.5m GRP for Sewerage Network Zone	21	21-Dec-25	10-Jan-26	25-Feb-26 A	12-Oct-26	$360,238.37	$54,035.76	100%
MOD-SWN-	Backfilling 1.5m GRP for Sewerage Network Zone 2	15	26-Jan-26	09-Feb-26	27-Oct-26	11-Nov-26	$160,105.94	$160,105.94	100%
MOD-SWN-	Excavation 1.5m GRP for Sewerage Network Zone 2	21	19-Oct-25	08-Nov-25	12-Feb-26 A	05-Oct-26	$120,079.46	$12,007.95	100%
MOD-SWN-	Lean Concrete / Bedding 1.5m GRP for Sewerage Network Zone 2	21	09-Nov-25	29-Nov-25	14-Feb-26 A	07-Oct-26	$80,052.97	$9,606.36	100%

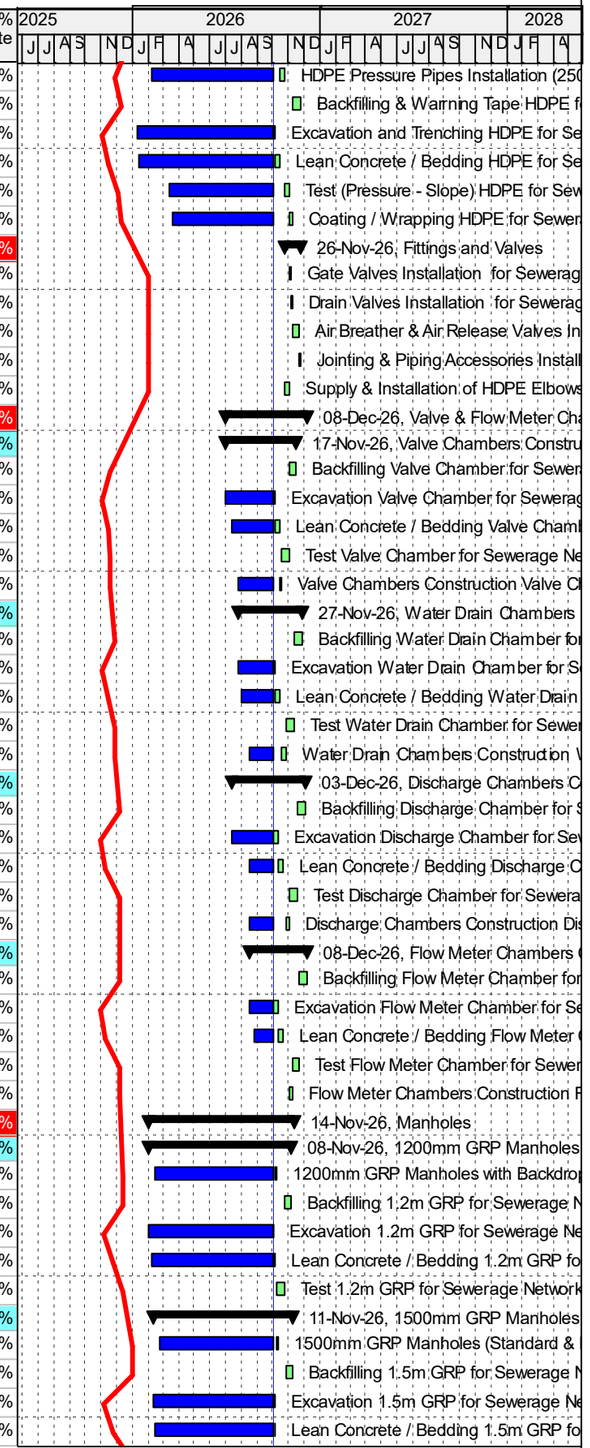


Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary

TASK filter: Schedule %.

© Oracle Corporation

Development of Phase One – Part Two – Third Industrial


Activity ID	Activity Name	Original Duration	BL Project Start	BL Project Finish	Start	Finish	Budgeted Total Cost	Remaining Total Cost	Schedule % Complete
MOD-SWN-	Test 1.5m GRP for Sewerage Network Zone 2	15	11-Jan-26	25-Jan-26	12-Oct-26	27-Oct-26	$80,052.97	$80,052.97	100%
1800mm GRP Manholes (Standard & Backdrop)		265	19-Oct-25	26-Feb-26	14-Feb-26 A	13-Nov-26	$39,936.34	$15,016.06	100%
MOD-SWN-	1800mm GRP Manholes (Standard & Backdrop) 1.8m GRP for Sewerage Network Zone	17	11-Jan-26	27-Jan-26	28-Feb-26 A	14-Oct-26	$17,971.35	$2,156.56	100%
MOD-SWN-	Backfilling 1.8m GRP for Sewerage Network Zone 2	15	12-Feb-26	26-Feb-26	29-Oct-26	13-Nov-26	$7,987.27	$7,987.27	100%
MOD-SWN-	Excavation 1.8m GRP for Sewerage Network Zone 2	21	19-Oct-25	08-Nov-25	14-Feb-26 A	04-Oct-26	$5,990.45	$479.24	100%
MOD-SWN-	Lean Concrete / Bedding 1.8m GRP for Sewerage Network Zone 2	21	09-Nov-25	29-Nov-25	16-Feb-26 A	06-Oct-26	$3,993.63	$399.36	100%
MOD-SWN-	Test 1.8m GRP for Sewerage Network Zone 2	15	28-Jan-26	11-Feb-26	14-Oct-26	29-Oct-26	$3,993.63	$3,993.63	100%
2000mm GRP Manholes (Standard & Backdrop)		266	19-Oct-25	04-Mar-26	14-Feb-26 A	14-Nov-26	$12,647.05	$4,736.32	100%
MOD-SWN-	2000mm GRP Manholes (Standard & Backdrop) 2m GRP for Sewerage Network Zone 2	6	28-Jan-26	02-Feb-26	22-Mar-26 A	15-Oct-26	$5,691.17	$682.94	100%
MOD-SWN-	Backfilling 2m GRP for Sewerage Network Zone 2	15	18-Feb-26	04-Mar-26	30-Oct-26	14-Nov-26	$2,529.41	$2,529.41	100%
MOD-SWN-	Excavation 2m GRP for Sewerage Network Zone 2	21	19-Oct-25	08-Nov-25	14-Feb-26 A	04-Oct-26	$1,897.06	$132.79	100%
MOD-SWN-	Lean Concrete / Bedding 2m GRP for Sewerage Network Zone 2	21	09-Nov-25	29-Nov-25	16-Mar-26 A	06-Oct-26	$1,264.70	$126.47	100%
MOD-SWN-	Test 2m GRP for Sewerage Network Zone 2	15	03-Feb-26	17-Feb-26	15-Oct-26	30-Oct-26	$1,264.70	$1,264.70	100%
Rainwater Drainage Network Zone 2		319	24-Oct-25	18-Jan-26	01-Dec-25 A	10-Nov-26	6,111,372.1	$2,565,524.76	100%
Pipe Laying Works		87	24-Oct-25	05-Jan-26	01-Dec-25 A	07-Oct-26	$632,822.65	$33,326.28	100%
Supply & Installation of uPVC Pipes (250–300mm dia)		35	14-Nov-25	13-Dec-25	01-Dec-25 A	04-Oct-26	$565,416.95	$28,270.85	100%
MOD-RWN-	Laying of uPVC pipe UPVC for Rainwater Drainage Network Zone 2	19	14-Nov-25	02-Dec-25	01-Dec-25 A	03-Oct-26	$339,250.17	$3,392.50	100%
MOD-RWN-	Coating / Wrapping UPVC for Rainwater Drainage Network Zone 2	2	06-Dec-25	07-Dec-25	04-Jan-26 A	03-Oct-26	$75,388.93	$7,538.89	100%
MOD-RWN-	Test (Pressure-slope) UPVC for Rainwater Drainage Network Zone 2	3	03-Dec-25	05-Dec-25	04-Jan-26 A	03-Oct-26	$75,388.93	$3,769.45	100%
MOD-RWN-	Backfilling & Warning Tape UPVC for Rainwater Drainage Network Zone 2	8	06-Dec-25	13-Dec-25	04-Jan-26 A	04-Oct-26	$75,388.93	$13,570.01	100%
uPVC Connection Pipes (150mm dia)		87	24-Oct-25	05-Jan-26	01-Dec-25 A	07-Oct-26	$67,405.71	$5,055.43	100%
MOD-RWN-	Lean Concrete / bedding material UPVC Con. for Rainwater Drainage Network Zone 2	3	24-Oct-25	26-Oct-25	01-Dec-25 A	03-Oct-26	$4,212.86	$210.64	100%
MOD-RWN-	Lay & connect UPVC Con. for Rainwater Drainage Network Zone 2	8	03-Dec-25	10-Dec-25	09-Dec-25 A	03-Oct-26	$37,915.71	$1,895.79	100%
MOD-RWN-	Test (Pressure-slope) UPVC Con. for Rainwater Drainage Network Zone 2	3	11-Dec-25	13-Dec-25	02-Jan-26 A	03-Oct-26	$8,425.71	$842.57	100%
MOD-RWN-	Backfilling & compaction UPVC Con. for Rainwater Drainage Network Zone 2	2	04-Jan-26	05-Jan-26	04-Jan-26 A	07-Oct-26	$8,425.71	$842.57	100%
MOD-RWN-	Coating / Wrapping UPVC Con. for Rainwater Drainage Network Zone 2	21	14-Dec-25	03-Jan-26	12-Jan-26 A	07-Oct-26	$8,425.71	$1,263.86	100%
Precast Concrete Box Culverts		143	03-Nov-25	18-Jan-26	18-Apr-26 A	09-Nov-26	2,104,171.7	$1,276,272.64	100%
Box Culverts (500x500mm to 3500x800mm)		143	03-Nov-25	18-Jan-26	25-Apr-26 A	09-Nov-26	2,067,068.4	$1,253,491.52	100%
MOD-RWN-	Surface finishing Box culvert for Rainwater Drainage Network Zone 2	3	15-Jan-26	18-Jan-26	05-Nov-26	09-Nov-26	$63,602.11	$63,602.11	100%
MOD-RWN-	Excavation to required depth Box culvert for Rainwater Drainage Network Zone 2	10	03-Nov-25	27-Nov-25	25-Apr-26 A	04-Oct-26	$530,017.55	$79,502.63	100%
MOD-RWN-	Dewatering and trench shoring Box culvert for Rainwater Drainage Network Zone 2	7	27-Nov-25	06-Dec-25	27-Apr-26 A	06-Oct-26	$424,014.04	$148,404.92	100%
MOD-RWN-	Bedding preparation (gravel/lean concrete) Box culvert for Rainwater Drainage Network Z	6	06-Dec-25	13-Dec-25	30-Apr-26 A	10-Oct-26	$159,005.27	$71,552.37	100%
MOD-RWN-	Installation of box culvert units Box culvert for Rainwater Drainage Network Zone 2	5	13-Dec-25	25-Dec-25	10-Oct-26	15-Oct-26	$636,021.07	$636,021.07	100%
MOD-RWN-	Alignment and joint sealing Box culvert for Rainwater Drainage Network Zone 2	4	25-Dec-25	30-Dec-25	15-Oct-26	20-Oct-26	$74,202.46	$74,202.46	100%
MOD-RWN-	Construct headwalls/wing walls (if needed) Box culvert for Rainwater Drainage Network Z	7	30-Dec-25	07-Jan-26	20-Oct-26	28-Oct-26	$106,003.51	$106,003.51	100%
MOD-RWN-	Backfilling and compaction Box culvert for Rainwater Drainage Network Zone 2	6	07-Jan-26	14-Jan-26	28-Oct-26	04-Nov-26	$74,202.46	$74,202.46	100%
Tube Culverts at Road Intersections		11	30-Nov-25	13-Dec-25	18-Apr-26 A	10-Oct-26	$25,056.68	$11,275.51	100%
MOD-RWN-	Trench excavation under road Tube culvert for Rainwater Drainage Network Zone 2	11	30-Nov-25	13-Dec-25	18-Apr-26 A	10-Oct-26	$25,056.68	$11,275.51	100%
Box Culverts at Road Intersections		137	18-Dec-25	18-Jan-26	02-May-26 A	03-Nov-26	$12,046.63	$11,505.62	100%
MOD-RWN-	Place bedding material for Rainwater Drainage Network Zone 2	1	18-Dec-25	20-Dec-25	02-May-26 A	04-Oct-26	$1,082.03	$541.02	100%
MOD-RWN-	Install precast box culvert for Rainwater Drainage Network Zone 2	4	20-Dec-25	24-Dec-25	05-Oct-26	08-Oct-26	$9,377.62	$9,377.62	100%
MOD-RWN-	Construct connection chambers (if needed) for Rainwater Drainage Network Zone 2	1	24-Dec-25	25-Dec-25	10-Oct-26	10-Oct-26	$1,082.03	$1,082.03	100%
MOD-RWN-	Joint treatment and testing for Rainwater Drainage Network Zone 2	12	25-Dec-25	08-Jan-26	11-Oct-26	24-Oct-26	$288.54	$288.54	100%
MOD-RWN-	Backfilling and surface reinstatement for Rainwater Drainage Network Zone 2	8	10-Jan-26	18-Jan-26	25-Oct-26	03-Nov-26	$216.41	$216.41	100%
Manholes		189	13-Dec-25	18-Jan-26	05-Jan-26 A	10-Nov-26	1,519,251.3	$865,020.28	100%
Circular GRP Manholes (1200–1800mm dia)		174	17-Dec-25	18-Jan-26	05-Jan-26 A	22-Oct-26	$441,407.90	$111,838.58	100%
MOD-RWN-	Dewatering and safety barriers Circular Manhole for Rainwater Drainage Network Zone 2	7	17-Dec-25	25-Dec-25	05-Jan-26 A	11-Oct-26	$139,512.34	$20,926.85	100%
MOD-RWN-	Concrete base construction Circular Manhole for Rainwater Drainage Network Zone 2	5	25-Dec-25	31-Dec-25	06-Jan-26 A	12-Oct-26	$137,225.25	$20,583.79	100%
MOD-RWN-	Install GRP manhole shaft sections Circular Manhole for Rainwater Drainage Network Zo	8	31-Dec-25	10-Jan-26	07-Jan-26 A	14-Oct-26	$114,354.38	$28,588.59	100%
MOD-RWN-	Place slab and cover frame Circular Manhole for Rainwater Drainage Network Zone 2	3	10-Jan-26	13-Jan-26	06-Jul-26 A	17-Oct-26	$34,306.31	$25,729.74	100%

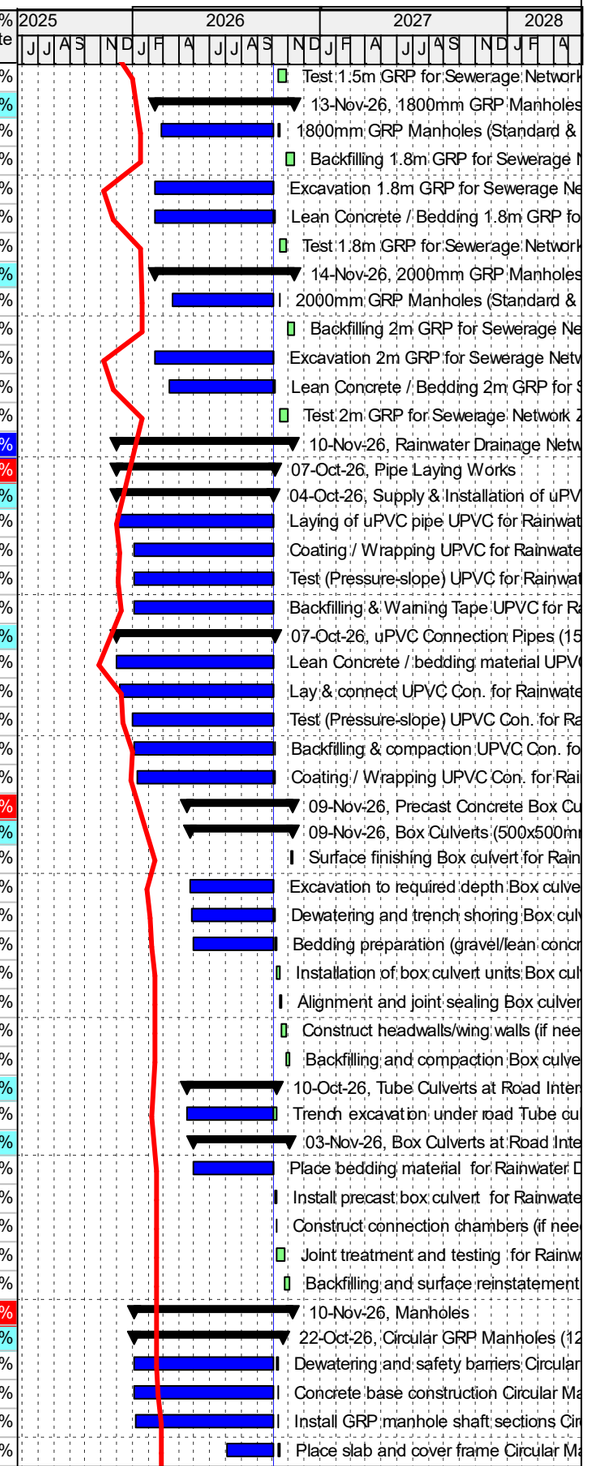

© Oracle Corporation

Development of Phase One – Part Two – Third Industrial


Activity ID	Activity Name	Original Duration	BL Project Start	BL Project Finish	Start	Finish	Budgeted Total Cost	Remaining Total Cost	Schedule % Complete
MOD-RWN-	Waterproofing Circular Manhole for Rainwater Drainage Network Zone 2	2	13-Jan-26	15-Jan-26	17-Oct-26	19-Oct-26	$9,148.35	$9,148.35	100%
MOD-RWN-	Backfilling and compaction Circular Manhole for Rainwater Drainage Network Zone 2	2	17-Jan-26	18-Jan-26	20-Oct-26	22-Oct-26	$6,861.26	$6,861.26	100%
Concrete Manholes for 1500x1500 Box Pipes		112	18-Dec-25	11-Jan-26	16-Feb-26 A	25-Oct-26	$684,193.29	$367,798.20	100%
MOD-RWN-	Base slab and wall shuttering Concrete Manhole 1.5x1.5 for Rainwater Drainage Networl	4	18-Dec-25	23-Dec-25	16-Feb-26 A	11-Oct-26	$216,247.62	$54,061.90	100%
MOD-RWN-	Wall reinforcement and casting Concrete Manhole 1.5x1.5 for Rainwater Drainage Netw	6	23-Dec-25	30-Dec-25	01-Mar-26 A	14-Oct-26	$212,702.58	$85,081.03	100%
MOD-RWN-	Roof slab with openings Concrete Manhole 1.5x1.5 for Rainwater Drainage Network Zon	3	30-Dec-25	03-Jan-26	05-Jul-26 A	17-Oct-26	$177,252.15	$150,664.32	100%
MOD-RWN-	Masonry/benching works inside Concrete Manhole 1.5x1.5 for Rainwater Drainage Netw	2	03-Jan-26	05-Jan-26	17-Oct-26	19-Oct-26	$53,175.64	$53,175.64	100%
MOD-RWN-	Install cover and frame Concrete Manhole 1.5x1.5 for Rainwater Drainage Network Zone	2	05-Jan-26	07-Jan-26	19-Oct-26	21-Oct-26	$14,180.17	$14,180.17	100%
MOD-RWN-	Backfill in layers Concrete Manhole 1.5x1.5 for Rainwater Drainage Network Zone 2	3	07-Jan-26	11-Jan-26	21-Oct-26	25-Oct-26	$10,635.13	$10,635.13	100%
Concrete Manholes for 1000x1000 Box Pipes		130	13-Dec-25	15-Jan-26	02-Mar-26 A	10-Nov-26	$393,650.15	$385,383.50	100%
MOD-RWN-	Base slab and wall shuttering Concrete Manhole 1x1 for Rainwater Drainage Network Zo	2	17-Dec-25	20-Dec-25	12-Oct-26	14-Oct-26	$120,063.30	$120,063.30	100%
MOD-RWN-	Wall reinforcement and casting Concrete Manhole 1x1 for Rainwater Drainage Network Z	5	20-Dec-25	25-Dec-25	14-Oct-26	20-Oct-26	$118,095.04	$118,095.04	100%
MOD-RWN-	Roof slab with openings Concrete Manhole 1x1 for Rainwater Drainage Network Zone 2	6	25-Dec-25	01-Jan-26	20-Oct-26	27-Oct-26	$98,412.54	$98,412.54	100%
MOD-RWN-	Masonry/benching works inside Concrete Manhole 1x1 for Rainwater Drainage Network Z	5	01-Jan-26	07-Jan-26	27-Oct-26	02-Nov-26	$29,523.76	$29,523.76	100%
MOD-RWN-	Install cover and frame Concrete Manhole 1x1 for Rainwater Drainage Network Zone 2	4	07-Jan-26	12-Jan-26	02-Nov-26	07-Nov-26	$7,873.00	$7,873.00	100%
MOD-RWN-	Backfill in layers Concrete Manhole 1x1 for Rainwater Drainage Network Zone 2	3	12-Jan-26	15-Jan-26	07-Nov-26	10-Nov-26	$5,904.75	$5,904.75	100%
MOD-RWN-	Excavation Concrete Manhole 1x1 for Rainwater Drainage Network Zone 2	4	13-Dec-25	17-Dec-25	02-Mar-26 A	12-Oct-26	$13,777.76	$5,511.10	100%
Gully Outfalls to Swales		196	24-Dec-25	18-Jan-26	01-Feb-26 A	25-Oct-26	$325,492.82	$88,802.93	100%
Gully Outfalls to Swales		187	28-Dec-25	18-Jan-26	07-Feb-26 A	14-Oct-26	$254,733.51	$41,747.99	100%
MOD-RWN-	Excavate outfall channel Gully Outfall to Swales for Rainwater Drainage Network Zone 2	5	28-Dec-25	03-Jan-26	07-Feb-26 A	10-Oct-26	$56,607.45	$2,830.37	100%
MOD-RWN-	Place concrete apron or pipes Gully Outfall to Swales for Rainwater Drainage Network Zo	7	03-Jan-26	11-Jan-26	15-Feb-26 A	11-Oct-26	$127,366.76	$6,368.34	100%
MOD-RWN-	Provide slope protection (riprap) Gully Outfall to Swales for Rainwater Drainage Network Z	4	11-Jan-26	15-Jan-26	20-Feb-26 A	11-Oct-26	$42,455.59	$4,245.56	100%
MOD-RWN-	Compact and shape terrain Gully Outfall to Swales for Rainwater Drainage Network Zone	2	17-Jan-26	18-Jan-26	12-Oct-26	14-Oct-26	$28,303.72	$28,303.72	100%
Riprap Works & Protection		128	24-Dec-25	14-Jan-26	01-Feb-26 A	25-Oct-26	$70,759.31	$47,054.94	100%
MOD-RWN-	Lay filter fabric/membrane for Rainwater Drainage Network Zone 2	3	24-Dec-25	28-Dec-25	01-Feb-26 A	11-Oct-26	$7,075.93	$2,830.37	100%
MOD-RWN-	Place riprap/stone layer for Rainwater Drainage Network Zone 2	7	28-Dec-25	05-Jan-26	17-Feb-26 A	15-Oct-26	$38,917.62	$19,458.81	100%
MOD-RWN-	Compact edges for Rainwater Drainage Network Zone 2	5	05-Jan-26	11-Jan-26	15-Oct-26	21-Oct-26	$14,151.86	$14,151.86	100%
MOD-RWN-	Ensure hydraulic flow direction for Rainwater Drainage Network Zone 2	3	11-Jan-26	14-Jan-26	21-Oct-26	25-Oct-26	$10,613.90	$10,613.90	100%
Backfilling & Bedding		41	27-Nov-25	06-Jan-26	01-Dec-25 A	12-Oct-26	1,529,633.5	$302,102.63	100%
Gravel Bedding & Filter Cloth for uPVC Drain Pipes		41	27-Nov-25	06-Jan-26	01-Dec-25 A	12-Oct-26	1,529,633.5	$302,102.63	100%
MOD-RWN-	Final fill and trench restoration for Rainwater Drainage Network Zone 2	8	28-Dec-25	06-Jan-26	01-Dec-25 A	12-Oct-26	$152,963.36	$45,889.01	100%
MOD-RWN-	Line trench with filter cloth for Rainwater Drainage Network Zone 2	6	27-Nov-25	04-Dec-25	23-Dec-25 A	05-Oct-26	$152,963.36	$15,296.34	100%
MOD-RWN-	Place and compact gravel bedding for Rainwater Drainage Network Zone 2	4	04-Dec-25	09-Dec-25	03-Jan-26 A	05-Oct-26	$305,926.71	$36,711.21	100%
MOD-RWN-	Lay pipe within gravel zone for Rainwater Drainage Network Zone 2	9	09-Dec-25	20-Dec-25	03-Jan-26 A	07-Oct-26	$688,335.11	$144,550.37	100%
MOD-RWN-	Wrap filter cloth above pipe for Rainwater Drainage Network Zone 2	7	20-Dec-25	28-Dec-25	03-Jan-26 A	10-Oct-26	$229,445.04	$59,655.71	100%
Potable Water Network Zone 2		309	09-Nov-25	13-Jan-26	01-Jan-26 A	25-Nov-26	2,832,238.8	$421,758.87	100%
Pipe Installation Works		62	09-Nov-25	14-Dec-25	01-Jan-26 A	04-Oct-26	1,603,785.8	$60,141.97	100%
MOD-PWN-PI-	Lean Concrete / Pipe Bedding Preparation for Potable Water Network Zone 2	4	09-Nov-25	12-Nov-25	01-Jan-26 A	03-Oct-26	$100,236.61	$3,007.10	100%
MOD-PWN-PI-	HDPE Pipe Laying (200 mm to 710 mm) for Potable Water Network Zone 2	21	13-Nov-25	03-Dec-25	04-Jan-26 A	03-Oct-26	$902,129.52	$27,063.89	100%
MOD-PWN-PI-	Test (Pressure-slope) for Potable Water Network Zone 2	3	04-Dec-25	06-Dec-25	05-Jan-26 A	03-Oct-26	$200,473.23	$10,023.66	100%
MOD-PWN-PI-	Coating / Wrapping for Potable Water Network Zone 2	5	07-Dec-25	11-Dec-25	15-Feb-26 A	04-Oct-26	$200,473.23	$10,023.66	100%
MOD-PWN-PI-	Backfilling & Warning Tape for Potable Water Network Zone 2	3	12-Dec-25	14-Dec-25	23-Feb-26 A	04-Oct-26	$200,473.23	$10,023.66	100%
Valve Installation & Chambers		117	09-Nov-25	31-Dec-25	01-Apr-26 A	17-Oct-26	$632,606.85	$147,460.66	100%
MOD-PWN-VC	Butterfly Valves (355, 500, 630 mm) for Potable Water Network Zone 2	12	07-Dec-25	20-Dec-25	18-Apr-26 A	04-Oct-26	$75,912.82	$6,832.15	100%
MOD-PWN-VC	3-exit (2 x 2.5-inch and 1 x 4-inch) dry vacuum cylinder detachable fire nozzle for Potabl	12	07-Dec-25	20-Dec-25	22-Apr-26 A	04-Oct-26	$82,238.89	$13,158.22	100%
MOD-PWN-VC	Valve Chamber Excavation for Potable Water Network Zone 2	12	09-Nov-25	22-Nov-25	01-Apr-26 A	03-Oct-26	$158,151.71	$12,652.14	100%
MOD-PWN-VC	RC Slab, Walls, or Precast Chambers for Potable Water Network Zone 2	15	23-Nov-25	09-Dec-25	07-Apr-26 A	05-Oct-26	$126,521.37	$11,386.92	100%
MOD-PWN-VC	Fixing Covers, Gratings, Frames for Potable Water Network Zone 2	6	21-Dec-25	27-Dec-25	05-Oct-26	12-Oct-26	$63,260.68	$63,260.68	100%
MOD-PWN-VC	Tagging & Painting for Potable Water Network Zone 2	4	28-Dec-25	31-Dec-25	12-Oct-26	17-Oct-26	$31,630.34	$31,630.34	100%

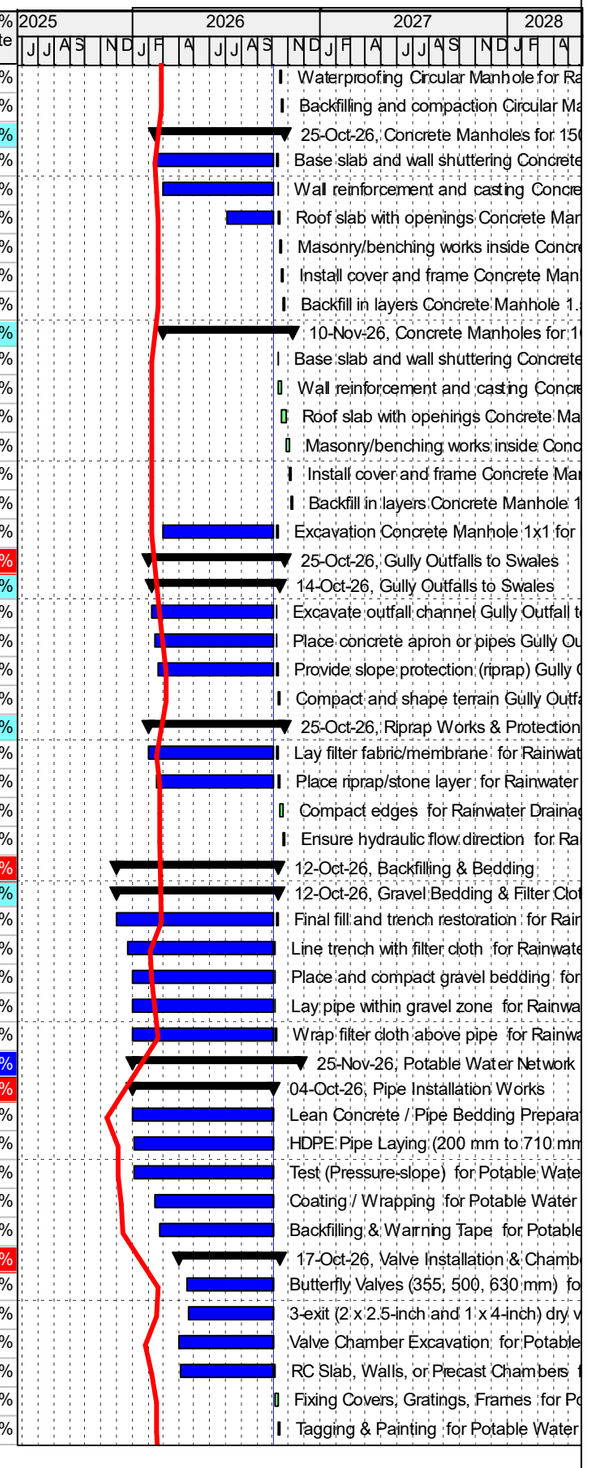

© Oracle Corporation

Development of Phase One – Part Two – Third Industrial

Activity ID	Activity Name	Original Duration	BL Project Start	BL Project Finish	Start	Finish	Budgeted Total Cost	Remaining Total Cost	Schedule % Complete
MOD-PWN-VC	Gate Valves (225–710 mm) for Potable Water Network Zone 2	12	07-Dec-25	20-Dec-25	14-Apr-26 A	04-Oct-26	$94,891.03	$8,540.19	100%
Flow Meter Installation		74	23-Nov-25	13-Jan-26	30-Aug-26 A	25-Nov-26	$123,072.32	$84,304.54	100%
MOD-PWN-FM	RC or Precast Chamber Construction for Potable Water Network Zone 2	7	02-Dec-25	09-Dec-25	01-Sep-26 A	10-Oct-26	$18,460.85	$10,338.07	100%
MOD-PWN-FM	Flowmeter Installation & Pipe Integration for Potable Water Network Zone 2	12	18-Dec-25	31-Dec-25	29-Oct-26	12-Nov-26	$43,075.31	$43,075.31	100%
MOD-PWN-FM	Wiring/Cabling if applicable for Potable Water Network Zone 2	8	01-Jan-26	10-Jan-26	12-Nov-26	22-Nov-26	$18,460.85	$18,460.85	100%
MOD-PWN-FM	Calibration & Commissioning for Potable Water Network Zone 2	3	11-Jan-26	13-Jan-26	22-Nov-26	25-Nov-26	$6,153.62	$6,153.62	100%
MOD-PWN-FM	Chamber Excavation (280 mm, 300 mm, 500 mm, 800 mm) for Potable Water Network	8	23-Nov-25	01-Dec-25	30-Aug-26 A	05-Oct-26	$36,921.69	$6,276.69	100%
Washout & Air Valve Chambers		97	29-Nov-25	07-Jan-26	13-May-26 A	12-Oct-26	$472,773.86	$129,851.71	100%
MOD-PWN-W/	Pipe Work for Potable Water Network Zone 2	14	29-Nov-25	14-Dec-25	13-May-26 A	05-Oct-26	$175,212.80	$26,281.92	100%
MOD-PWN-W/	Washout (Valve + Outlet) Installation for Potable Water Network Zone 2	10	15-Dec-25	25-Dec-25	17-May-26 A	07-Oct-26	$129,538.51	$25,907.70	100%
MOD-PWN-W/	Air Valve Rooms (Valve + Outlet) Installation for Potable Water Network Zone 2	5	27-Dec-25	31-Dec-25	11-Aug-26 A	08-Oct-26	$90,150.20	$27,045.06	100%
MOD-PWN-W/	Covers, Ladders & Tags for Potable Water Network Zone 2	4	01-Jan-26	05-Jan-26	17-Sep-26 A	10-Oct-26	$38,936.18	$11,680.85	100%
MOD-PWN-W/	Backfilling & Final Finishing for Potable Water Network Zone 2	2	06-Jan-26	07-Jan-26	10-Oct-26	12-Oct-26	$38,936.18	$38,936.18	100%
Irrigation Network Zone 2		288	09-Nov-25	18-Jan-26	01-Dec-25 A	08-Nov-26	1,107,130.0	$140,225.60	100%
Excavation, Pipe Laying & Backfilling		101	09-Nov-25	14-Dec-25	01-Dec-25 A	05-Oct-26	$874,055.20	$81,942.67	100%
MOD-IRN-EB-3	Lean Concrete / Pipe Bedding with Type B Material for Irrigation Network Zone 2	9	09-Nov-25	17-Nov-25	01-Dec-25 A	03-Oct-26	$54,628.45	$1,638.85	100%
MOD-IRN-EB-3	HDPE Pipe Laying (125 mm to 630 mm) for Irrigation Network Zone 2	21	18-Nov-25	08-Dec-25	01-Jan-26 A	03-Oct-26	$491,656.05	$14,749.68	100%
MOD-IRN-EB-3	Test (Pressure-slope) for Irrigation Network Zone 2	2	09-Dec-25	10-Dec-25	06-Jan-26 A	04-Oct-26	$109,256.90	$10,925.69	100%
MOD-IRN-EB-3	Coating / Wrapping for Irrigation Network Zone 2	2	11-Dec-25	12-Dec-25	20-Feb-26 A	04-Oct-26	$109,256.90	$10,925.69	100%
MOD-IRN-EB-3	Backfilling & Warning Tape for Irrigation Network Zone 2	2	13-Dec-25	14-Dec-25	28-Feb-26 A	05-Oct-26	$109,256.90	$43,702.76	100%
Valves and Appurtenances		69	07-Dec-25	29-Dec-25	05-Feb-26 A	07-Oct-26	$127,197.68	$23,163.08	100%
MOD-IRN-VA-1	Supply & Installation of Valves (Butterfly Valve) for Irrigation Network Zone 2	8	11-Dec-25	20-Dec-25	27-Feb-26 A	04-Oct-26	$35,634.32	$6,057.83	100%
MOD-IRN-VA-2	Installation of Flanges, Bolts, Collars, Nuts for Irrigation Network Zone 2	4	21-Dec-25	24-Dec-25	28-Feb-26 A	05-Oct-26	$5,087.91	$1,017.58	100%
MOD-IRN-VA-3	Valve Pressure Testing for Irrigation Network Zone 2	2	25-Dec-25	27-Dec-25	04-Jul-26 A	06-Oct-26	$3,179.94	$1,589.97	100%
MOD-IRN-VA-4	Support Brackets/Anchor Blocks for Irrigation Network Zone 2	2	28-Dec-25	29-Dec-25	07-Jul-26 A	07-Oct-26	$4,451.92	$2,671.15	100%
MOD-IRN-VA-5	Supply & Installation of Valves (Gate Valve) for Irrigation Network Zone 2	8	07-Dec-25	15-Dec-25	05-Feb-26 A	04-Oct-26	$78,843.59	$11,826.54	100%
Valve Rooms		3	15-Jan-26	18-Jan-26	13-Jul-26 A	04-Oct-26	$6,014.80	$1,202.96	100%
MOD-IRN-VR-6	Backfilling and Finishing Valve Chamber for Irrigation Network Zone 2	3	15-Jan-26	18-Jan-26	13-Jul-26 A	04-Oct-26	$6,014.80	$1,202.96	100%
Washout Chambers		15	13-Jan-26	18-Jan-26	22-Jun-26 A	05-Oct-26	$28,122.71	$5,624.54	100%
MOD-IRN-WC-	Manhole Frame, Cover & Ladder Fixing Washout Chamber for Irrigation Network Zone 2	3	13-Jan-26	15-Jan-26	22-Jun-26 A	05-Oct-26	$21,092.04	$5,273.01	100%
MOD-IRN-WC-	Backfilling & Reinstatement Washout Chamber for Irrigation Network Zone 2	2	17-Jan-26	18-Jan-26	05-Jul-26 A	05-Oct-26	$7,030.68	$351.53	100%
Flow Meter Chambers		124	28-Dec-25	18-Jan-26	26-May-26 A	08-Nov-26	$71,739.70	$28,292.34	100%
MOD-IRN-FC-1	RCC Base & Wall Construction Flow Meter Chamber for Irrigation Network Zone 2	5	28-Dec-25	01-Jan-26	26-May-26 A	05-Oct-26	$8,967.46	$1,345.12	100%
MOD-IRN-FC-2	Flow Meter Installation (280, 300, 500 mm) Flow Meter Chamber for Irrigation Network Zo	5	03-Jan-26	07-Jan-26	01-Jul-26 A	31-Oct-26	$31,386.12	$5,649.50	100%
MOD-IRN-FC-3	Integration with Pipework Flow Meter Chamber for Irrigation Network Zone 2	2	08-Jan-26	10-Jan-26	02-Jul-26 A	31-Oct-26	$13,451.19	$3,362.80	100%
MOD-IRN-FC-4	Testing & Calibration Flow Meter Chamber for Irrigation Network Zone 2	4	11-Jan-26	14-Jan-26	31-Oct-26	04-Nov-26	$13,451.19	$13,451.19	100%
MOD-IRN-FC-5	Cover and Access Arrangement Flow Meter Chamber for Irrigation Network Zone 2	3	15-Jan-26	18-Jan-26	04-Nov-26	08-Nov-26	$4,483.73	$4,483.73	100%
Rainwater Collection Ponds Zone 2		213	22-Jan-26	27-Sep-26	17-Nov-25 A	01-Apr-27	$751,276.36	$414,992.14	100%
Excavation for Rainwater Drainage Pond		51	22-Jan-26	14-Mar-26	08-Jun-26 A	09-Jan-27	$108,808.35	$14,432.61	100%
Deep excavation, backfill, disposal for pond formation		51	22-Jan-26	14-Mar-26	08-Jun-26 A	09-Jan-27	$108,808.35	$14,432.61	100%
MOD-RCP-E	Excavate in layers to final depth for Rainwater Collection Ponds Zone 2	12	22-Jan-26	04-Feb-26	08-Jun-26 A	02-Jan-27	$34,390.20	$3,439.02	100%
MOD-RCP-E	Dewater during excavation for Rainwater Collection Ponds Zone 2	5	05-Feb-26	10-Feb-26	07-Jul-26 A	03-Jan-27	$33,826.43	$3,382.64	100%
MOD-RCP-E	Place warning tapes for Rainwater Collection Ponds Zone 2	6	11-Feb-26	19-Feb-26	21-Jul-26 A	03-Jan-27	$8,456.61	$845.66	100%
MOD-RCP-E	Dispose of rock/materials to approved dump area for Rainwater Collection Ponds Zone 2	7	19-Feb-26	05-Mar-26	01-Aug-26 A	04-Jan-27	$28,188.69	$2,818.87	100%
MOD-RCP-E	Backfill selected areas as per design for Rainwater Collection Ponds Zone 2	2	07-Mar-26	10-Mar-26	04-Jan-27	06-Jan-27	$2,255.10	$2,255.10	100%
MOD-RCP-E	Final trimming and profiling for Rainwater Collection Ponds Zone 2	2	10-Mar-26	14-Mar-26	06-Jan-27	09-Jan-27	$1,691.32	$1,691.32	100%
Backfilling Works		165	08-Jun-26	23-Aug-26	17-Nov-25 A	21-Jan-27	$241,295.27	$56,704.39	100%
MOD-RCP-BW	Place in layers not exceeding 300mm for Rainwater Collection Ponds Zone 2	21	25-Jun-26	20-Jul-26	17-Nov-25 A	10-Jan-27	$84,453.34	$16,890.67	100%
MOD-RCP-BW	Compact each layer to required density for Rainwater Collection Ponds Zone 2	20	20-Jul-26	12-Aug-26	25-Nov-25 A	14-Jan-27	$60,323.82	$12,064.76	100%
MOD-RCP-BW	Conduct field density tests for Rainwater Collection Ponds Zone 2	4	12-Aug-26	17-Aug-26	01-Aug-26 A	16-Jan-27	$36,194.29	$10,858.29	100%

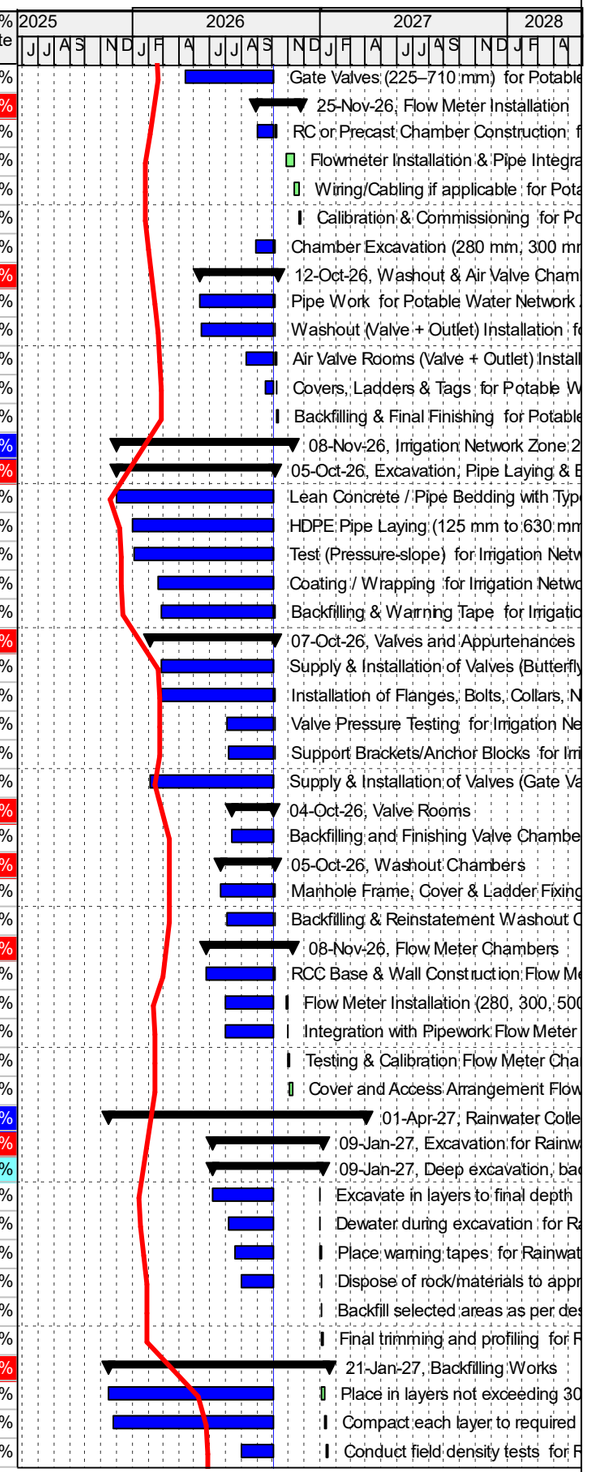


Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary

TASK filter: Schedule %.

© Oracle Corporation

Development of Phase One – Part Two – Third Industrial


Activity ID	Activity Name	Original Duration	BL Project Start	BL Project Finish	Start	Finish	Budgeted Total Cost	Remaining Total Cost	Schedule % Complete
MOD-RCP-BW	Final leveling and approval for Rainwater Collection Ponds Zone 2	5	17-Aug-26	23-Aug-26	16-Jan-27	21-Jan-27	$12,064.76	$12,064.76	100%
MOD-RCP-BW	Select material from excavation or import approved material for Rainwater Collection Po	15	08-Jun-26	25-Jun-26	18-Nov-25 A	05-Jan-27	$48,259.05	$4,825.91	100%
Geotextile & Bedding		213	04-Jul-26	10-Sep-26	17-Jan-26 A	23-Mar-27	$368,470.27	$311,152.67	100%
Installation of geotextile lining and coarse sand bedding		213	04-Jul-26	10-Sep-26	17-Jan-26 A	23-Mar-27	$368,470.27	$311,152.67	100%
MOD-RCP-(	Lay HDPE geotextile membrane over compacted soil for Rainwater Collection Ponds Zo	21	04-Jul-26	28-Jul-26	17-Jan-26 A	19-Jan-27	$143,293.99	$85,976.40	100%
MOD-RCP-(	Place 500mm thick coarse sand bedding for Rainwater Collection Ponds Zone 2	21	28-Jul-26	22-Aug-26	22-Jul-26 A	17-Feb-27	$122,823.42	$122,823.42	100%
MOD-RCP-(	Compact and level bedding for Rainwater Collection Ponds Zone 2	17	22-Aug-26	10-Sep-26	17-Feb-27	23-Mar-27	$102,352.85	$102,352.85	100%
Concrete Structures		8	16-Sep-26	27-Sep-26	20-Sep-26 A	01-Apr-27	$32,702.46	$32,702.46	100%
Construction of pond slab, walls, vertical structures		8	16-Sep-26	27-Sep-26	20-Sep-26 A	01-Apr-27	$32,702.46	$32,702.46	100%
MOD-RCP-(	Install formwork and reinforcement for Rainwater Collection Ponds Zone 2	8	16-Sep-26	27-Sep-26	20-Sep-26 A	01-Apr-27	$32,702.46	$32,702.46	100%
Road Crossing Zone 2		159	22-Jan-26	07-Oct-26	31-Dec-26	27-Jul-27	1,644,651.2	$1,644,651.20	99.17%
uPVC Road Crossing Pipes		68	22-Jan-26	22-Jun-26	31-Dec-26	07-Apr-27	1,202,844.7	$1,202,844.75	100%
Installation of uPVC pipes of various diameters crossing roadways		68	22-Jan-26	22-Jun-26	31-Dec-26	07-Apr-27	1,202,844.7	$1,202,844.75	100%
MOD-ROC-F	Demarcation and traffic diversion (if required) for Road Crossing Zone 2	6	22-Jan-26	28-Jan-26	31-Dec-26	07-Jan-27	$60,142.24	$60,142.24	100%
MOD-ROC-F	Saw cutting and removal of asphalt (if applicable) for Road Crossing Zone 2	12	29-Jan-26	11-Feb-26	07-Jan-27	21-Jan-27	$120,284.48	$120,284.48	100%
MOD-ROC-F	Excavation across road width to required depth for Road Crossing Zone 2	10	12-Feb-26	26-Mar-26	21-Jan-27	02-Feb-27	$180,426.71	$180,426.71	100%
MOD-ROC-F	Preparation of trench base with compacted bedding for Road Crossing Zone 2	5	26-Mar-26	13-Apr-26	02-Feb-27	09-Feb-27	$120,284.48	$120,284.48	100%
MOD-ROC-F	Laying of uPVC pipe (300mm, 315mm, 400mm, 600mm dia) for Road Crossing Zone 2	10	13-Apr-26	07-May-26	09-Feb-27	02-Mar-27	$481,137.90	$481,137.90	100%
MOD-ROC-F	Placement of supports and protection around the pipe for Road Crossing Zone 2	5	07-May-26	19-May-26	02-Mar-27	15-Mar-27	$120,284.48	$120,284.48	100%
MOD-ROC-F	Testing of installed pipeline for Road Crossing Zone 2	6	19-May-26	26-May-26	16-Mar-27	22-Mar-27	$30,071.12	$30,071.12	100%
MOD-ROC-F	Backfilling and compaction in layers for Road Crossing Zone 2	8	26-May-26	15-Jun-26	23-Mar-27	31-Mar-27	$60,142.24	$60,142.24	100%
MOD-ROC-F	Reinstatement of road surface for Road Crossing Zone 2	6	15-Jun-26	22-Jun-26	01-Apr-27	07-Apr-27	$30,071.12	$30,071.12	100%
GRP Road Crossing Pipes		91	22-Jun-26	07-Oct-26	08-Apr-27	27-Jul-27	$441,806.44	$441,806.44	96.92%
Installation of GRP pipes (800mm–1000mm dia) for road crossings		91	22-Jun-26	07-Oct-26	08-Apr-27	27-Jul-27	$441,806.44	$441,806.44	96.92%
MOD-ROC-(	Set out location and coordinate with road authority for Road Crossing Zone 2	5	22-Jun-26	28-Jun-26	08-Apr-27	13-Apr-27	$22,656.74	$22,656.74	100%
MOD-ROC-(	Excavate trench across road at designed depth for Road Crossing Zone 2	12	28-Jun-26	12-Jul-26	14-Apr-27	27-Apr-27	$45,313.48	$45,313.48	100%
MOD-ROC-(	Lay compacted granular bedding for Road Crossing Zone 2	16	12-Jul-26	30-Jul-26	28-Apr-27	20-May-27	$67,970.22	$67,970.22	100%
MOD-ROC-(	Install GRP pipe (800mm & 1000mm dia) for Road Crossing Zone 2	21	30-Jul-26	24-Aug-26	22-May-27	14-Jun-27	$181,253.92	$181,253.92	100%
MOD-ROC-(	Provide structural supports and closure at both ends for Road Crossing Zone 2	9	24-Aug-26	03-Sep-26	15-Jun-27	24-Jun-27	$45,313.48	$45,313.48	100%
MOD-ROC-(	Perform leak testing as per specifications for Road Crossing Zone 2	5	03-Sep-26	09-Sep-26	26-Jun-27	30-Jun-27	$11,328.37	$11,328.37	100%
MOD-ROC-(	Backfill and compact in layers for Road Crossing Zone 2	15	09-Sep-26	28-Sep-26	01-Jul-27	18-Jul-27	$45,313.48	$45,313.48	100%
MOD-ROC-(	Reinstate road surface (asphalt/concrete) for Road Crossing Zone 2	8	28-Sep-26	07-Oct-26	19-Jul-27	27-Jul-27	$22,656.74	$22,656.74	40%
Zone 1		601	19-Oct-25	25-Oct-26	03-Sep-25 A	27-Jul-27	28,991,897.5	$8,533,031.30	97.17%
Sewerage Network Zone 1		381	19-Oct-25	25-Oct-26	22-Nov-25 A	05-Jan-27	4,055,768.2	$2,358,921.00	83.35%
Pipework: Supply, Installation, and Testing		114	19-Oct-25	03-Feb-26	22-Nov-25 A	10-Oct-26	$208,367.13	$11,460.19	100%
HDPE Pressure Pipes Installation (250mm–630mm)		114	19-Oct-25	03-Feb-26	22-Nov-25 A	10-Oct-26	$208,367.13	$11,460.19	100%
MOD-SWN-	HDPE Pressure Pipes Installation (250mm–630mm) HDPE for Sewerage Network Zone	21	30-Nov-25	20-Dec-25	27-Nov-25 A	05-Oct-26	$93,765.21	$2,812.96	100%
MOD-SWN-	Backfilling & Warrning Tape HDPE for Sewerage Network Zone 1	15	20-Jan-26	03-Feb-26	05-Feb-26 A	10-Oct-26	$20,836.71	$5,209.18	100%
MOD-SWN-	Excavation and Trenching HDPE for Sewerage Network Zone 1	21	19-Oct-25	08-Nov-25	22-Nov-25 A	03-Oct-26	$41,673.43	$833.47	100%
MOD-SWN-	Lean Concrete / Bedding HDPE for Sewerage Network Zone 1	21	09-Nov-25	29-Nov-25	02-Feb-26 A	04-Oct-26	$10,418.36	$520.92	100%
MOD-SWN-	Test (Pressure - Slope) HDPE for Sewerage Network Zone 1	15	21-Dec-25	04-Jan-26	03-Feb-26 A	05-Oct-26	$20,836.71	$1,041.84	100%
MOD-SWN-	Coating / Wrapping HDPE for Sewerage Network Zone 1	15	05-Jan-26	19-Jan-26	11-Dec-25 A	06-Oct-26	$20,836.71	$1,041.84	100%
Fittings and Valves		27	21-Dec-25	20-Jan-26	05-Oct-26	05-Nov-26	$61,422.41	$61,422.41	100%
MOD-SWN-FV-	Supply & Installation of HDPE Elbows for Sewerage Network Zone 1	6	21-Dec-25	27-Dec-25	05-Oct-26	12-Oct-26	$13,652.43	$13,652.43	100%
MOD-SWN-FV-	Gate Valves Installation for Sewerage Network Zone 1	4	28-Dec-25	31-Dec-25	12-Oct-26	17-Oct-26	$9,660.60	$9,660.60	100%
MOD-SWN-FV-	Drain Valves Installation for Sewerage Network Zone 1	4	01-Jan-26	05-Jan-26	17-Oct-26	21-Oct-26	$8,785.65	$8,785.65	100%
MOD-SWN-FV-	Air Breather & Air Release Valves Installation for Sewerage Network Zone 1	10	06-Jan-26	17-Jan-26	21-Oct-26	02-Nov-26	$23,181.49	$23,181.49	100%
MOD-SWN-FV-	Jointing & Piping Accessories Installation for Sewerage Network Zone 1	3	18-Jan-26	20-Jan-26	02-Nov-26	05-Nov-26	$6,142.24	$6,142.24	100%
Valve & Flow Meter Chambers		153	19-Oct-25	10-Feb-26	01-Jun-26 A	17-Dec-26	$99,848.78	$62,171.03	100%
Valve Chambers Construction		71	19-Oct-25	04-Jan-26	01-Jun-26 A	29-Nov-26	$13,788.12	$10,341.09	100%

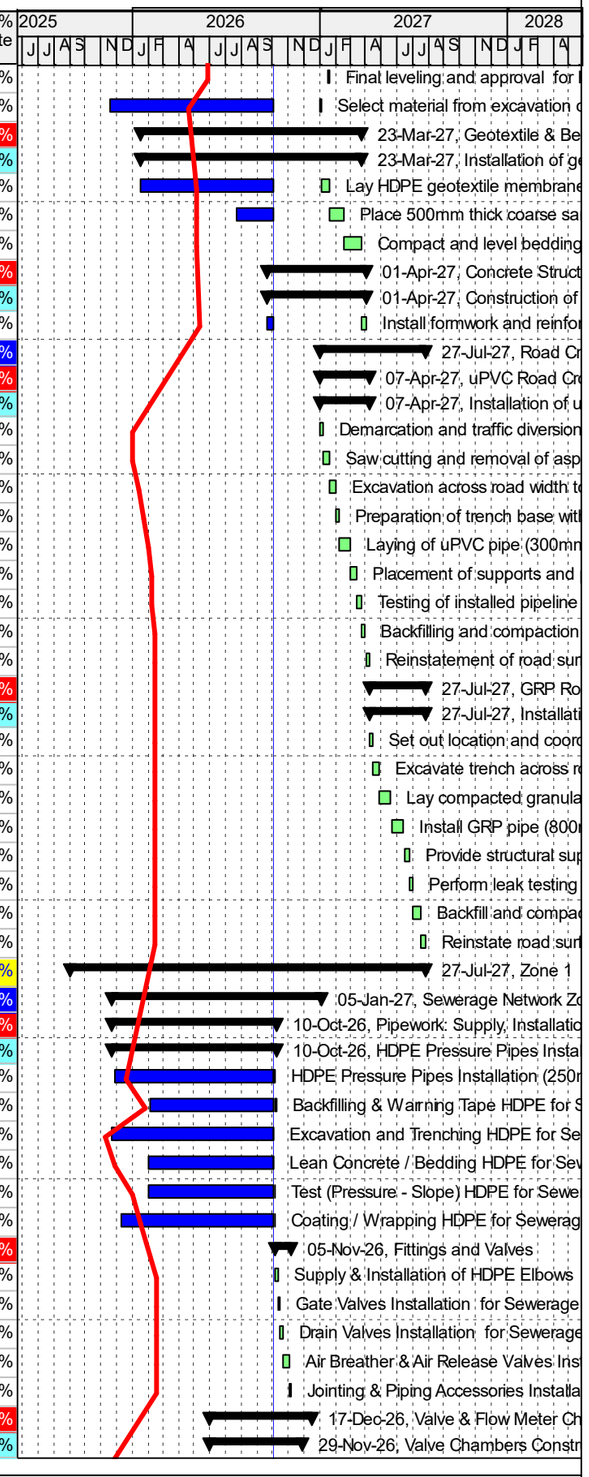

© Oracle Corporation

Development of Phase One – Part Two – Third Industrial

Activity ID	Activity Name	Original Duration	BL Project Start	BL Project Finish	Start	Finish	Budgeted Total Cost	Remaining Total Cost	Schedule % Complete
MOD-SWN-	Backfilling Valve Chamber for Sewerage Network Zone 1	15	21-Dec-25	04-Jan-26	14-Nov-26	29-Nov-26	$2,757.62	$2,757.62	100%
MOD-SWN-	Excavation Valve Chamber for Sewerage Network Zone 1	21	19-Oct-25	08-Nov-25	01-Jun-26 A	13-Oct-26	$2,068.22	$1,034.11	100%
MOD-SWN-	Lean Concrete / Bedding Valve Chamber for Sewerage Network Zone 1	21	09-Nov-25	29-Nov-25	09-Jun-26 A	26-Oct-26	$1,378.81	$827.29	100%
MOD-SWN-	Test Valve Chamber for Sewerage Network Zone 1	15	06-Dec-25	20-Dec-25	30-Oct-26	14-Nov-26	$1,378.81	$1,378.81	100%
MOD-SWN-	Valve Chambers Construction Valve Chamber for Sewerage Network Zone 1	6	30-Nov-25	05-Dec-25	23-Jun-26 A	30-Oct-26	$6,204.65	$4,343.26	100%
Water Drain Chambers Construction		133	19-Oct-25	23-Jan-26	11-Jul-26 A	27-Nov-26	$44,788.55	$22,618.22	100%
MOD-SWN-	Backfilling Water Drain Chamber for Sewerage Network Zone 1	15	09-Jan-26	23-Jan-26	12-Nov-26	27-Nov-26	$8,957.71	$8,957.71	100%
MOD-SWN-	Excavation Water Drain Chamber for Sewerage Network Zone 1	21	19-Oct-25	08-Nov-25	11-Jul-26 A	09-Oct-26	$6,718.28	$2,015.48	100%
MOD-SWN-	Lean Concrete / Bedding Water Drain Chamber for Sewerage Network Zone 1	21	09-Nov-25	29-Nov-25	22-Jul-26 A	17-Oct-26	$4,478.86	$1,791.54	100%
MOD-SWN-	Test Water Drain Chamber for Sewerage Network Zone 1	15	25-Dec-25	08-Jan-26	01-Aug-26 A	12-Nov-26	$4,478.86	$1,791.54	100%
MOD-SWN-	Water Drain Chambers Construction Water Drain Chamber for Sewerage Network Zone	19	06-Dec-25	24-Dec-25	29-Jul-26 A	06-Nov-26	$20,154.85	$8,061.94	100%
Discharge Chambers Construction		88	19-Oct-25	05-Feb-26	13-Jul-26 A	15-Dec-26	$31,287.23	$23,465.42	100%
MOD-SWN-	Backfilling Discharge Chamber for Sewerage Network Zone 1	15	22-Jan-26	05-Feb-26	01-Dec-26	15-Dec-26	$6,257.45	$6,257.45	100%
MOD-SWN-	Excavation Discharge Chamber for Sewerage Network Zone 1	21	19-Oct-25	08-Nov-25	13-Jul-26 A	13-Oct-26	$4,693.08	$2,346.54	100%
MOD-SWN-	Lean Concrete / Bedding Discharge Chamber for Sewerage Network Zone 1	21	09-Nov-25	29-Nov-25	14-Jul-26 A	26-Oct-26	$3,128.72	$1,877.23	100%
MOD-SWN-	Test Discharge Chamber for Sewerage Network Zone 1	15	07-Jan-26	21-Jan-26	16-Nov-26	30-Nov-26	$3,128.72	$3,128.72	100%
MOD-SWN-	Discharge Chambers Construction Discharge Chamber for Sewerage Network Zone 1	13	25-Dec-25	06-Jan-26	29-Jul-26 A	15-Nov-26	$14,079.25	$9,855.48	100%
Flow Meter Chambers Construction		153	19-Oct-25	10-Feb-26	11-Jul-26 A	17-Dec-26	$9,984.88	$5,746.30	100%
MOD-SWN-	Backfilling Flow Meter Chamber for Sewerage Network Zone 1	15	27-Jan-26	10-Feb-26	03-Dec-26	17-Dec-26	$1,996.98	$1,996.98	100%
MOD-SWN-	Excavation Flow Meter Chamber for Sewerage Network Zone 1	21	19-Oct-25	08-Nov-25	11-Jul-26 A	10-Oct-26	$1,497.73	$554.16	100%
MOD-SWN-	Lean Concrete / Bedding Flow Meter Chamber for Sewerage Network Zone 1	21	09-Nov-25	29-Nov-25	28-Jul-26 A	19-Oct-26	$998.49	$399.40	100%
MOD-SWN-	Test Flow Meter Chamber for Sewerage Network Zone 1	15	12-Jan-26	26-Jan-26	18-Nov-26	02-Dec-26	$998.49	$998.49	100%
MOD-SWN-	Flow Meter Chambers Construction Flow Meter Chamber for Sewerage Network Zone 1	5	07-Jan-26	11-Jan-26	01-Aug-26 A	17-Nov-26	$4,493.20	$1,797.28	100%
Manholes		288	19-Oct-25	08-Jan-26	01-Jan-26 A	24-Oct-26	1,698,371.3	$562,160.92	100%
1200mm GRP Manholes with Backdrop		288	19-Oct-25	24-Dec-25	01-Jan-26 A	24-Oct-26	$845,258.26	$279,780.48	100%
MOD-SWN-	1200mm GRP Manholes with Backdrop 1.2m GRP for Sewerage Network Zone 1	21	14-Nov-25	04-Dec-25	04-Jan-26 A	04-Oct-26	$380,366.22	$19,018.31	100%
MOD-SWN-	Backfilling 1.2m GRP for Sewerage Network Zone 1	15	10-Dec-25	24-Dec-25	09-Oct-26	24-Oct-26	$169,051.65	$169,051.65	100%
MOD-SWN-	Excavation 1.2m GRP for Sewerage Network Zone 1	21	19-Oct-25	08-Nov-25	01-Jan-26 A	03-Oct-26	$126,788.74	$3,803.66	100%
MOD-SWN-	Lean Concrete / Bedding 1.2m GRP for Sewerage Network Zone 1	5	09-Nov-25	13-Nov-25	03-Jan-26 A	03-Oct-26	$84,525.83	$3,381.03	100%
MOD-SWN-	Test 1.2m GRP for Sewerage Network Zone 1	5	05-Dec-25	09-Dec-25	04-Oct-26	09-Oct-26	$84,525.83	$84,525.83	100%
1500mm GRP Manholes (Standard & Backdrop)		288	19-Oct-25	29-Dec-25	03-Jan-26 A	24-Oct-26	$800,529.72	$264,975.34	100%
MOD-SWN-	1500mm GRP Manholes (Standard & Backdrop) 1.5m GRP for Sewerage Network Zone	21	19-Nov-25	09-Dec-25	14-Feb-26 A	04-Oct-26	$360,238.37	$18,011.92	100%
MOD-SWN-	Backfilling 1.5m GRP for Sewerage Network Zone 1	15	15-Dec-25	29-Dec-25	09-Oct-26	24-Oct-26	$160,105.94	$160,105.94	100%
MOD-SWN-	Excavation 1.5m GRP for Sewerage Network Zone 1	21	19-Oct-25	08-Nov-25	03-Jan-26 A	03-Oct-26	$120,079.46	$3,602.38	100%
MOD-SWN-	Lean Concrete / Bedding 1.5m GRP for Sewerage Network Zone 1	5	09-Nov-25	13-Nov-25	03-Feb-26 A	03-Oct-26	$80,052.97	$3,202.12	100%
MOD-SWN-	Test 1.5m GRP for Sewerage Network Zone 1	5	10-Dec-25	14-Dec-25	04-Oct-26	09-Oct-26	$80,052.97	$80,052.97	100%
1800mm GRP Manholes (Standard & Backdrop)		288	19-Oct-25	30-Dec-25	05-Jan-26 A	24-Oct-26	$39,936.34	$13,218.93	100%
MOD-SWN-	1800mm GRP Manholes (Standard & Backdrop) 1.8m GRP for Sewerage Network Zone	17	24-Nov-25	10-Dec-25	22-Feb-26 A	04-Oct-26	$17,971.35	$898.57	100%
MOD-SWN-	Backfilling 1.8m GRP for Sewerage Network Zone 1	15	16-Dec-25	30-Dec-25	09-Oct-26	24-Oct-26	$7,987.27	$7,987.27	100%
MOD-SWN-	Excavation 1.8m GRP for Sewerage Network Zone 1	21	19-Oct-25	08-Nov-25	05-Jan-26 A	03-Oct-26	$5,990.45	$179.71	100%
MOD-SWN-	Lean Concrete / Bedding 1.8m GRP for Sewerage Network Zone 1	5	09-Nov-25	13-Nov-25	03-Feb-26 A	03-Oct-26	$3,993.63	$159.75	100%
MOD-SWN-	Test 1.8m GRP for Sewerage Network Zone 1	5	11-Dec-25	15-Dec-25	04-Oct-26	09-Oct-26	$3,993.63	$3,993.63	100%
2000mm GRP Manholes (Standard & Backdrop)		288	19-Oct-25	08-Jan-26	06-Jan-26 A	24-Oct-26	$12,647.05	$4,186.17	100%
MOD-SWN-	2000mm GRP Manholes (Standard & Backdrop) 2m GRP for Sewerage Network Zone 1	21	29-Nov-25	19-Dec-25	25-Feb-26 A	04-Oct-26	$5,691.17	$284.56	100%
MOD-SWN-	Backfilling 2m GRP for Sewerage Network Zone 1	15	25-Dec-25	08-Jan-26	09-Oct-26	24-Oct-26	$2,529.41	$2,529.41	100%
MOD-SWN-	Excavation 2m GRP for Sewerage Network Zone 1	21	19-Oct-25	08-Nov-25	06-Jan-26 A	03-Oct-26	$1,897.06	$56.91	100%
MOD-SWN-	Lean Concrete / Bedding 2m GRP for Sewerage Network Zone 1	5	09-Nov-25	13-Nov-25	05-Feb-26 A	03-Oct-26	$1,264.70	$50.59	100%
MOD-SWN-	Test 2m GRP for Sewerage Network Zone 1	5	20-Dec-25	24-Dec-25	04-Oct-26	09-Oct-26	$1,264.70	$1,264.70	100%
Pumping Stations		199	06-Nov-25	25-Oct-26	01-Jan-26 A	05-Jan-27	1,987,758.5	$1,661,706.45	66.04%

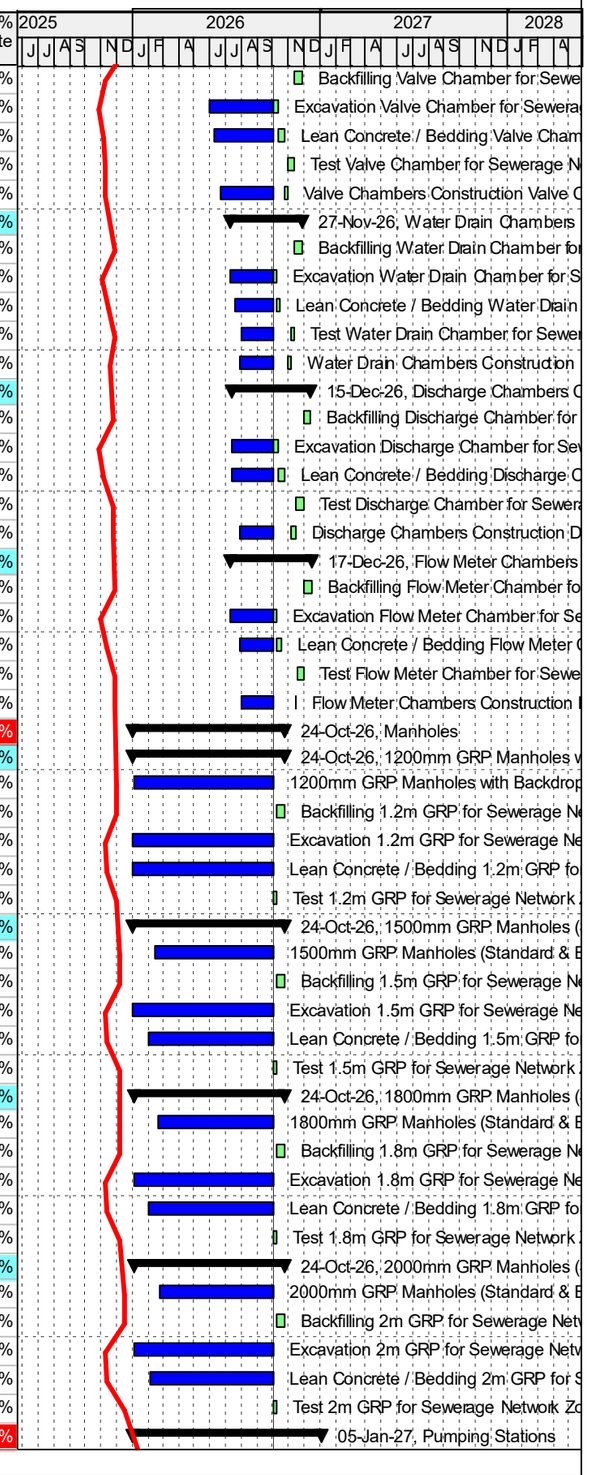


Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary

TASK filter: Schedule %.

© Oracle Corporation

Development of Phase One – Part Two – Third Industrial


Activity ID	Activity Name	Original Duration	BL Project Start	BL Project Finish	Start	Finish	Budgeted Total Cost	Remaining Total Cost	Schedule % Complete
Perimeter Walls & Gates		10	01-Dec-25	11-Dec-25	30-Jul-26 A	07-Oct-26	$37,635.25	$18,817.63	100%
MOD-SWN-	Main entrance gates – Each PS for Sewerage Network Zone 1	10	01-Dec-25	11-Dec-25	30-Jul-26 A	07-Oct-26	$27,650.44	$13,825.22	100%
MOD-SWN-	Personal entrance gate – Each PS for Sewerage Network Zone 1	4	01-Dec-25	04-Dec-25	31-Jul-26 A	04-Oct-26	$9,984.81	$4,992.41	100%
Odor Control System		25	31-Aug-26	25-Oct-26	30-Nov-26	29-Dec-26	$276,510.51	$276,510.51	56.96%
MOD-SWN-	Odor control system – All stations (PS1) for Sewerage Network Zone 1	10	31-Aug-26	28-Sep-26	30-Nov-26	12-Dec-26	$138,255.26	$138,255.26	100%
MOD-SWN-	Odor control system – All stations (PS2) for Sewerage Network Zone 1	15	28-Sep-26	25-Oct-26	12-Dec-26	29-Dec-26	$138,255.26	$138,255.26	13.91%
In-Line Booster Stations		21	28-Sep-26	22-Oct-26	12-Dec-26	05-Jan-27	$656,073.36	$656,073.36	15.24%
MOD-SWN-	In-Line Booster Stations - Civil Works for Sewerage Network Zone 1	21	28-Sep-26	22-Oct-26	12-Dec-26	05-Jan-27	$656,073.36	$656,073.36	15.24%
Engine/Motor Control Center Buildings		8	06-Nov-25	08-Dec-25	03-Oct-26	11-Oct-26	$45,941.19	$45,941.19	100%
MOD-SWN-	MCC Building – PS1 for Sewerage Network Zone 1	1	06-Nov-25	06-Nov-25	03-Oct-26	03-Oct-26	$3,888.46	$3,888.46	100%
MOD-SWN-	MCC Building – PS2 for Sewerage Network Zone 1	7	01-Dec-25	08-Dec-25	04-Oct-26	11-Oct-26	$42,052.73	$42,052.73	100%
Valves and Fittings (General Supply & Installation)		5	18-Dec-25	23-Dec-25	29-Oct-26	04-Nov-26	$23,484.26	$23,484.26	100%
MOD-SWN-	Valves, fittings & accessories – PS1 for Sewerage Network Zone 1	2	18-Dec-25	20-Dec-25	29-Oct-26	01-Nov-26	$6,720.76	$6,720.76	100%
MOD-SWN-	35mm raked bar SS 316 mesh – PS1 for Sewerage Network Zone 1	1	21-Dec-25	21-Dec-25	01-Nov-26	02-Nov-26	$4,838.91	$4,838.91	100%
MOD-SWN-	Valves, fittings, flow meters – PS2 for Sewerage Network Zone 1	2	22-Dec-25	23-Dec-25	02-Nov-26	04-Nov-26	$11,924.59	$11,924.59	100%
Pump Well and Valve Chambers		62	19-Nov-25	29-Jan-26	04-Oct-26	14-Dec-26	$442,703.31	$442,703.31	100%
MOD-SWN-	Pump well & valve chamber structure – PS1 (2 wells, 12m deep) for Sewerage Network	13	19-Nov-25	03-Dec-25	04-Oct-26	18-Oct-26	$74,197.09	$74,197.09	100%
MOD-SWN-	Concrete wall (5x5x1m) inside PS1 well for Sewerage Network Zone 1	7	04-Dec-25	11-Dec-25	19-Oct-26	26-Oct-26	$41,284.68	$41,284.68	100%
MOD-SWN-	35 mm raked bar SS 316 network chamber PS1 for Sewerage Network Zone 1	1	13-Dec-25	13-Dec-25	27-Oct-26	27-Oct-26	$2,688.28	$2,688.28	100%
MOD-SWN-	Valve chamber – PS1 for Sewerage Network Zone 1	6	14-Dec-25	20-Dec-25	28-Oct-26	03-Nov-26	$34,141.39	$34,141.39	100%
MOD-SWN-	Flow meter chamber – PS1 for Sewerage Network Zone 1	4	21-Dec-25	24-Dec-25	04-Nov-26	08-Nov-26	$20,216.04	$20,216.04	100%
MOD-SWN-	Pump well & valve chamber structure – PS2 (2 wells, 3m each, 9m depth) for Sewerage	14	04-Dec-25	20-Dec-25	19-Oct-26	03-Nov-26	$81,656.84	$81,656.84	100%
MOD-SWN-	Valve chamber – PS2 for Sewerage Network Zone 1	16	25-Dec-25	12-Jan-26	09-Nov-26	26-Nov-26	$97,546.82	$97,546.82	100%
MOD-SWN-	Flow meter chamber – PS2 for Sewerage Network Zone 1	15	13-Jan-26	29-Jan-26	28-Nov-26	14-Dec-26	$90,972.17	$90,972.17	100%
Odor Control System Base/Plinth		6	25-Dec-25	31-Dec-25	25-Oct-26	31-Oct-26	$16,590.51	$16,590.51	100%
MOD-SWN-	Concrete plinth below odor control – All PSs for Sewerage Network Zone 1	6	25-Dec-25	31-Dec-25	25-Oct-26	31-Oct-26	$16,590.51	$16,590.51	100%
Lighting Works		13	13-Dec-25	27-Dec-25	01-Jan-26 A	29-Oct-26	$384,043.12	$76,808.62	100%
MOD-SWN-	250W Flood Light installation – Each PS for Sewerage Network Zone 1	13	13-Dec-25	27-Dec-25	01-Jan-26 A	29-Oct-26	$384,043.12	$76,808.62	100%
Duct Works		7	04-Dec-25	11-Dec-25	19-Oct-26	26-Oct-26	$15,220.07	$15,220.07	100%
MOD-SWN-	uPVC duct Track 1 – All PSs for Sewerage Network Zone 1	1	04-Dec-25	04-Dec-25	19-Oct-26	19-Oct-26	$2,760.41	$2,760.41	100%
MOD-SWN-	uPVC duct Track 2 – All PSs for Sewerage Network Zone 1	2	06-Dec-25	07-Dec-25	20-Oct-26	21-Oct-26	$3,185.08	$3,185.08	100%
MOD-SWN-	uPVC duct Track 8 – All PSs for Sewerage Network Zone 1	4	08-Dec-25	11-Dec-25	22-Oct-26	26-Oct-26	$9,274.58	$9,274.58	100%
Grounding Works		3	13-Dec-25	15-Dec-25	27-Oct-26	29-Oct-26	$7,603.32	$7,603.32	100%
MOD-SWN-	Grounding pit – Each PS for Sewerage Network Zone 1	1	13-Dec-25	13-Dec-25	27-Oct-26	27-Oct-26	$1,690.17	$1,690.17	100%
MOD-SWN-	600x600 Cable pull pit – All PSs for Sewerage Network Zone 1	2	14-Dec-25	15-Dec-25	28-Oct-26	29-Oct-26	$5,913.15	$5,913.15	100%
Landscaping / Interlocking Tiles		21	06-Dec-25	29-Dec-25	05-Oct-26	28-Oct-26	$61,674.68	$61,674.68	100%
MOD-SWN-	Building perimeter interlock tiles for Sewerage Network Zone 1	17	06-Dec-25	24-Dec-25	05-Oct-26	24-Oct-26	$50,952.81	$50,952.81	100%
MOD-SWN-	Entrance road paving tiles for Sewerage Network Zone 1	4	25-Dec-25	29-Dec-25	25-Oct-26	28-Oct-26	$10,721.87	$10,721.87	100%
Pumping Station Internal Drainage Network		7	01-Dec-25	08-Dec-25	03-Oct-26	10-Oct-26	$20,278.98	$20,278.98	100%
MOD-SWN-	Internal surface drainage channels for Sewerage Network Zone 1	7	01-Dec-25	08-Dec-25	03-Oct-26	10-Oct-26	$20,278.98	$20,278.98	100%
Rainwater Drainage Network Zone 1		326	19-Oct-25	18-Jan-26	01-Oct-25 A	02-Nov-26	9,473,736.1	$1,935,891.37	100%
Pipe Laying Works		77	19-Oct-25	05-Jan-26	01-Oct-25 A	11-Oct-26	$817,082.11	$61,282.22	100%
Supply & Installation of uPVC Pipes (250–300mm dia)		77	19-Oct-25	13-Dec-25	01-Oct-25 A	06-Oct-26	$753,889.26	$52,772.25	100%
MOD-RWN-	Excavation to required depth UPVC for Rainwater Drainage Network Zone 1	21	19-Oct-25	08-Nov-25	01-Oct-25 A	04-Oct-26	$150,777.85	$7,538.89	100%
MOD-RWN-	Lean Concrete / Bedding UPVC for Rainwater Drainage Network Zone 1	5	09-Nov-25	13-Nov-25	05-Oct-25 A	04-Oct-26	$37,694.46	$1,884.72	100%
MOD-RWN-	Laying of uPVC pipe UPVC for Rainwater Drainage Network Zone 1	19	14-Nov-25	02-Dec-25	06-Oct-25 A	05-Oct-26	$339,250.17	$16,962.51	100%
MOD-RWN-	Coating / Wrapping UPVC for Rainwater Drainage Network Zone 1	2	06-Dec-25	07-Dec-25	08-Jan-26 A	05-Oct-26	$75,388.93	$7,538.89	100%
MOD-RWN-	Test (Pressure-slope) UPVC for Rainwater Drainage Network Zone 1	3	03-Dec-25	05-Dec-25	07-Jan-26 A	05-Oct-26	$75,388.93	$7,538.89	100%
MOD-RWN-	Backfilling & Warning Tape UPVC for Rainwater Drainage Network Zone 1	8	06-Dec-25	13-Dec-25	10-Jan-26 A	06-Oct-26	$75,388.93	$11,308.34	100%
uPVC Connection Pipes (150mm dia)		46	03-Dec-25	05-Jan-26	29-Dec-25 A	11-Oct-26	$63,192.85	$8,509.97	100%

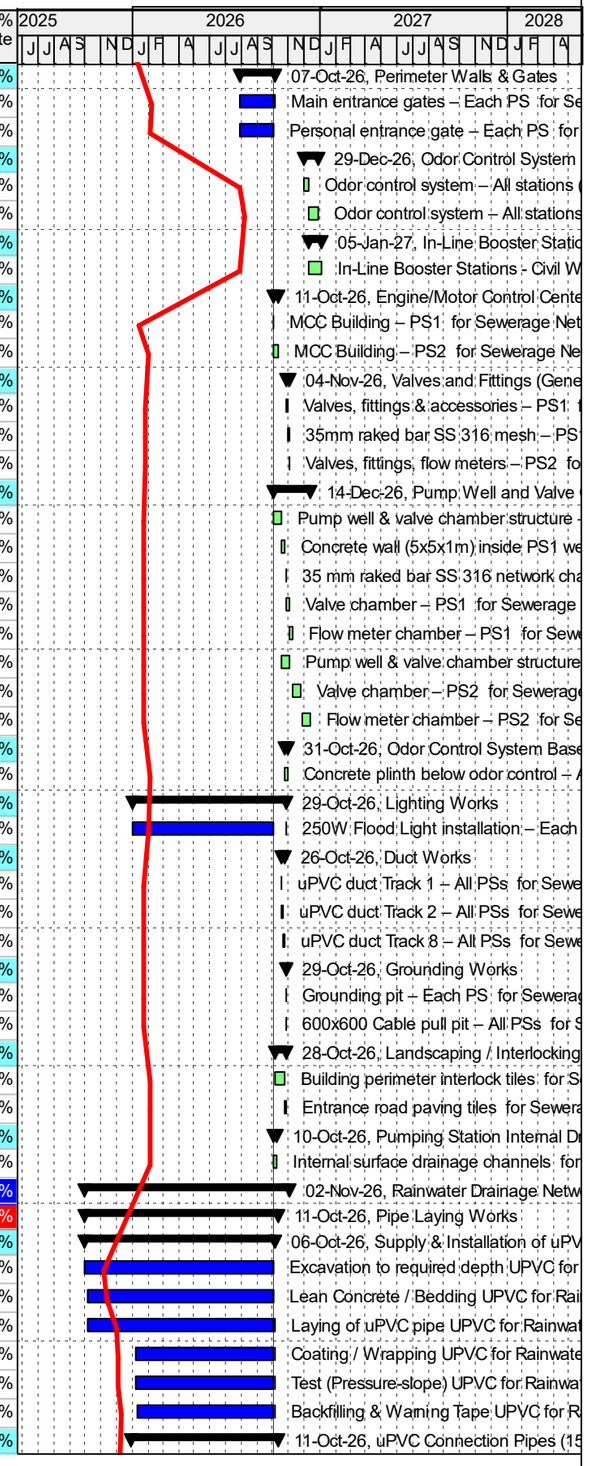

© Oracle Corporation

Development of Phase One – Part Two – Third Industrial

Activity ID	Activity Name	Original Duration	BL Project Start	BL Project Finish	Start	Finish	Budgeted Total Cost	Remaining Total Cost	Schedule % Complete
MOD-RWN-	Lay & connect UPVC Con. for Rainwater Drainage Network Zone 1	8	03-Dec-25	10-Dec-25	29-Dec-25 A	05-Oct-26	$37,915.71	$3,033.26	100%
MOD-RWN-	Test (Pressure-slope) UPVC Con. for Rainwater Drainage Network Zone 1	3	11-Dec-25	13-Dec-25	08-Jan-26 A	06-Oct-26	$8,425.71	$1,685.14	100%
MOD-RWN-	Backfilling & compaction UPVC Con. for Rainwater Drainage Network Zone 1	2	04-Jan-26	05-Jan-26	11-Jan-26 A	11-Oct-26	$8,425.71	$2,106.43	100%
MOD-RWN-	Coating / Wrapping UPVC Con. for Rainwater Drainage Network Zone 1	21	14-Dec-25	03-Jan-26	10-Jan-26 A	10-Oct-26	$8,425.71	$1,685.14	100%
Precast Concrete Box Culverts		138	02-Nov-25	06-Jan-26	18-Apr-26 A	01-Nov-26	2,230,580.0	$779,533.75	100%
Box Culverts (500x500mm to 3500x800mm)		134	02-Nov-25	06-Jan-26	18-Apr-26 A	27-Oct-26	2,067,068.4	$683,722.65	100%
MOD-RWN-	Excavation to required depth Box culvert for Rainwater Drainage Network Zone 1	5	02-Nov-25	10-Nov-25	18-Apr-26 A	03-Oct-26	$530,017.55	$79,502.63	100%
MOD-RWN-	Dewatering and trench shoring Box culvert for Rainwater Drainage Network Zone 1	5	10-Nov-25	19-Nov-25	22-Apr-26 A	04-Oct-26	$424,014.04	$84,802.81	100%
MOD-RWN-	Bedding preparation (gravel/lean concrete) Box culvert for Rainwater Drainage Network Z	4	19-Nov-25	24-Nov-25	24-Apr-26 A	05-Oct-26	$159,005.27	$47,701.58	100%
MOD-RWN-	Installation of box culvert units Box culvert for Rainwater Drainage Network Zone 1	8	25-Nov-25	11-Dec-25	28-Apr-26 A	10-Oct-26	$636,021.07	$190,806.32	100%
MOD-RWN-	Alignment and joint sealing Box culvert for Rainwater Drainage Network Zone 1	4	13-Dec-25	16-Dec-25	05-May-26 A	12-Oct-26	$74,202.46	$37,101.23	100%
MOD-RWN-	Construct headwalls/wing walls (if needed) Box culvert for Rainwater Drainage Network Z	5	17-Dec-25	25-Dec-25	12-Oct-26	18-Oct-26	$106,003.51	$106,003.51	100%
MOD-RWN-	Backfilling and compaction Box culvert for Rainwater Drainage Network Zone 1	5	27-Dec-25	03-Jan-26	18-Oct-26	24-Oct-26	$74,202.46	$74,202.46	100%
MOD-RWN-	Surface finishing Box culvert for Rainwater Drainage Network Zone 1	3	04-Jan-26	06-Jan-26	24-Oct-26	27-Oct-26	$63,602.11	$63,602.11	100%
Tube Culverts at Road Intersections		114	24-Nov-25	04-Jan-26	12-May-26 A	21-Oct-26	$149,445.20	$83,671.41	100%
MOD-RWN-	Pipe bedding and twin pipe alignment Tube culvert for Rainwater Drainage Network Zone	6	24-Nov-25	01-Dec-25	12-May-26 A	06-Oct-26	$13,423.22	$6,711.61	100%
MOD-RWN-	Pipe laying and jointing Tube culvert for Rainwater Drainage Network Zone 1	10	01-Dec-25	25-Dec-25	24-May-26 A	12-Oct-26	$118,124.35	$59,062.17	100%
MOD-RWN-	Backfilling and road reinstatement Tube culvert for Rainwater Drainage Network Zone 1	8	25-Dec-25	04-Jan-26	12-Oct-26	21-Oct-26	$17,897.63	$17,897.63	100%
Box Culverts at Road Intersections		127	30-Nov-25	01-Jan-26	16-May-26 A	01-Nov-26	$14,066.43	$12,139.69	100%
MOD-RWN-	Deep trench excavation with shoring for Rainwater Drainage Network Zone 1	1	30-Nov-25	01-Dec-25	16-May-26 A	03-Oct-26	$2,019.79	$363.56	100%
MOD-RWN-	Place bedding material for Rainwater Drainage Network Zone 1	1	01-Dec-25	02-Dec-25	05-Sep-26 A	04-Oct-26	$1,082.03	$811.52	100%
MOD-RWN-	Install precast box culvert for Rainwater Drainage Network Zone 1	4	02-Dec-25	07-Dec-25	04-Oct-26	08-Oct-26	$9,377.62	$9,377.62	100%
MOD-RWN-	Construct connection chambers (if needed) for Rainwater Drainage Network Zone 1	1	07-Dec-25	08-Dec-25	08-Oct-26	10-Oct-26	$1,082.03	$1,082.03	100%
MOD-RWN-	Joint treatment and testing for Rainwater Drainage Network Zone 1	10	08-Dec-25	22-Dec-25	10-Oct-26	21-Oct-26	$288.54	$288.54	100%
MOD-RWN-	Backfilling and surface reinstatement for Rainwater Drainage Network Zone 1	9	22-Dec-25	01-Jan-26	21-Oct-26	01-Nov-26	$216.41	$216.41	100%
Manholes		240	25-Nov-25	18-Jan-26	01-Jan-26 A	02-Nov-26	1,519,251.3	$510,279.59	100%
Circular GRP Manholes (1200–1800mm dia)		43	01-Dec-25	18-Jan-26	01-Jan-26 A	24-Oct-26	$441,407.90	$124,531.92	100%
MOD-RWN-	Dewatering and safety barriers Circular Manhole for Rainwater Drainage Network Zone 1	10	01-Dec-25	11-Dec-25	01-Jan-26 A	08-Oct-26	$139,512.34	$20,926.85	100%
MOD-RWN-	Concrete base construction Circular Manhole for Rainwater Drainage Network Zone 1	5	13-Dec-25	17-Dec-25	03-Jan-26 A	10-Oct-26	$137,225.25	$41,167.58	100%
MOD-RWN-	Install GRP manhole shaft sections Circular Manhole for Rainwater Drainage Network Zo	13	18-Dec-25	01-Jan-26	06-Jan-26 A	15-Oct-26	$114,354.38	$40,024.03	100%
MOD-RWN-	Place slab and cover frame Circular Manhole for Rainwater Drainage Network Zone 1	6	03-Jan-26	08-Jan-26	11-Jan-26 A	18-Oct-26	$34,306.31	$13,722.53	100%
MOD-RWN-	Waterproofing Circular Manhole for Rainwater Drainage Network Zone 1	5	10-Jan-26	14-Jan-26	12-Jan-26 A	21-Oct-26	$9,148.35	$4,574.18	100%
MOD-RWN-	Backfilling and compaction Circular Manhole for Rainwater Drainage Network Zone 1	3	15-Jan-26	18-Jan-26	13-Jan-26 A	24-Oct-26	$6,861.26	$4,116.76	100%
Concrete Manholes for 1500x1500 Box Pipes		234	01-Dec-25	17-Jan-26	03-Jan-26 A	26-Oct-26	$684,193.29	$207,030.51	100%
MOD-RWN-	Base slab and wall shuttering Concrete Manhole 1.5x1.5 for Rainwater Drainage Networl	7	01-Dec-25	08-Dec-25	03-Jan-26 A	08-Oct-26	$216,247.62	$43,249.52	100%
MOD-RWN-	Wall reinforcement and casting Concrete Manhole 1.5x1.5 for Rainwater Drainage Netw	8	09-Dec-25	17-Dec-25	15-Feb-26 A	11-Oct-26	$212,702.58	$53,175.64	100%
MOD-RWN-	Roof slab with openings Concrete Manhole 1.5x1.5 for Rainwater Drainage Network Zon	5	18-Dec-25	23-Dec-25	17-Feb-26 A	12-Oct-26	$177,252.15	$62,038.25	100%
MOD-RWN-	Masonry/benching works inside Concrete Manhole 1.5x1.5 for Rainwater Drainage Netw	4	24-Dec-25	28-Dec-25	21-Feb-26 A	14-Oct-26	$53,175.64	$26,587.82	100%
MOD-RWN-	Install cover and frame Concrete Manhole 1.5x1.5 for Rainwater Drainage Network Zone	6	05-Jan-26	11-Jan-26	24-Feb-26 A	20-Oct-26	$14,180.17	$11,344.14	100%
MOD-RWN-	Backfill in layers Concrete Manhole 1.5x1.5 for Rainwater Drainage Network Zone 1	5	12-Jan-26	17-Jan-26	20-Oct-26	26-Oct-26	$10,635.13	$10,635.13	100%
Concrete Manholes for 1000x1000 Box Pipes		202	25-Nov-25	12-Jan-26	01-Jan-26 A	02-Nov-26	$393,650.15	$178,717.17	100%
MOD-RWN-	Excavation Concrete Manhole 1x1 for Rainwater Drainage Network Zone 1	6	25-Nov-25	01-Dec-25	01-Jan-26 A	08-Oct-26	$13,777.76	$2,755.55	100%
MOD-RWN-	Base slab and wall shuttering Concrete Manhole 1x1 for Rainwater Drainage Network Zo	4	02-Dec-25	06-Dec-25	01-Feb-26 A	10-Oct-26	$120,063.30	$48,025.32	100%
MOD-RWN-	Wall reinforcement and casting Concrete Manhole 1x1 for Rainwater Drainage Network Z	7	07-Dec-25	14-Dec-25	01-Apr-26 A	13-Oct-26	$118,095.04	$47,238.02	100%
MOD-RWN-	Roof slab with openings Concrete Manhole 1x1 for Rainwater Drainage Network Zone 1	8	15-Dec-25	23-Dec-25	06-Apr-26 A	18-Oct-26	$98,412.54	$49,206.27	100%
MOD-RWN-	Masonry/benching works inside Concrete Manhole 1x1 for Rainwater Drainage Network Z	10	24-Dec-25	04-Jan-26	21-Apr-26 A	25-Oct-26	$29,523.76	$17,714.26	100%
MOD-RWN-	Install cover and frame Concrete Manhole 1x1 for Rainwater Drainage Network Zone 1	4	05-Jan-26	08-Jan-26	25-Oct-26	29-Oct-26	$7,873.00	$7,873.00	100%
MOD-RWN-	Backfill in layers Concrete Manhole 1x1 for Rainwater Drainage Network Zone 1	3	10-Jan-26	12-Jan-26	29-Oct-26	02-Nov-26	$5,904.75	$5,904.75	100%
Chambers and Catch Basins		2	13-Jan-26	14-Jan-26	02-May-26 A	10-Oct-26	$52,160.51	$2,086.42	100%

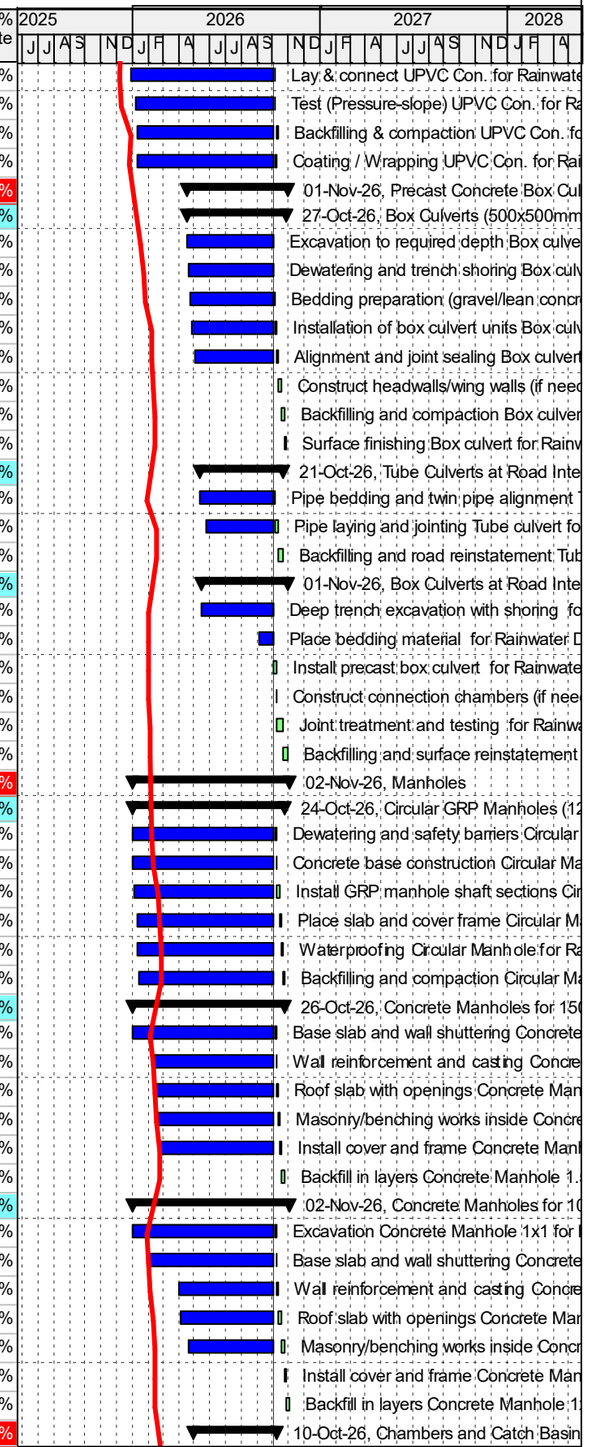


Actual Level of Effort · Actual Work · Remaining Work · Critical Remaining Work · Milestone · summary

TASK filter: Schedule %.

© Oracle Corporation

Development of Phase One – Part Two – Third Industrial

Activity ID	Activity Name	Original Duration	BL Project Start	BL Project Finish	Start	Finish	Budgeted Total Cost	Remaining Total Cost	Schedule % Complete
Rainwater Catch Basins		2	13-Jan-26	14-Jan-26	02-May-26 A	10-Oct-26	$52,160.51	$2,086.42	100%
MOD-RWN-	Backfill and surface finish Catch Basin for Rainwater Drainage Network Zone 1	2	13-Jan-26	14-Jan-26	02-May-26 A	10-Oct-26	$52,160.51	$2,086.42	100%
Gully Outfalls to Swales		67	27-Dec-25	15-Jan-26	07-Jan-26 A	13-Oct-26	$258,271.48	$38,846.86	100%
Gully Outfalls to Swales		66	27-Dec-25	07-Jan-26	07-Jan-26 A	11-Oct-26	$198,126.07	$20,237.16	100%
MOD-RWN-	Place concrete apron or pipes Gully Outfall to Swales for Rainwater Drainage Network Zc	5	27-Dec-25	31-Dec-25	07-Jan-26 A	10-Oct-26	$127,366.76	$6,368.34	100%
MOD-RWN-	Provide slope protection (riprap) Gully Outfall to Swales for Rainwater Drainage Network Z	4	01-Jan-26	05-Jan-26	01-Feb-26 A	10-Oct-26	$42,455.59	$4,245.56	100%
MOD-RWN-	Compact and shape terrain Gully Outfall to Swales for Rainwater Drainage Network Zone	2	06-Jan-26	07-Jan-26	02-Apr-26 A	11-Oct-26	$28,303.72	$9,623.27	100%
Riprap Works & Protection		27	03-Jan-26	15-Jan-26	01-Feb-26 A	13-Oct-26	$60,145.41	$18,609.70	100%
MOD-RWN-	Lay filter fabric/membrane for Rainwater Drainage Network Zone 1	2	03-Jan-26	04-Jan-26	01-Feb-26 A	10-Oct-26	$7,075.93	$1,415.19	100%
MOD-RWN-	Place riprap/stone layer for Rainwater Drainage Network Zone 1	7	05-Jan-26	12-Jan-26	28-Feb-26 A	12-Oct-26	$38,917.62	$10,118.58	100%
MOD-RWN-	Compact edges for Rainwater Drainage Network Zone 1	3	13-Jan-26	15-Jan-26	01-Apr-26 A	13-Oct-26	$14,151.86	$7,075.93	100%
Backfilling & Bedding		203	02-Nov-25	18-Jan-26	01-Jan-26 A	19-Oct-26	4,596,390.6	$543,862.54	100%
Backfilling Materials (Type A– 201–700mm Pipes)		197	10-Nov-25	18-Jan-26	01-Jan-26 A	13-Oct-26	3,066,757.0	$345,010.17	100%
MOD-RWN-	Place granular bedding under pipe for Rainwater Drainage Network Zone 1	9	10-Nov-25	20-Nov-25	01-Jan-26 A	03-Oct-26	$306,675.71	$3,066.76	100%
MOD-RWN-	Lay and align pipe for Rainwater Drainage Network Zone 1	21	20-Nov-25	15-Dec-25	01-Feb-26 A	04-Oct-26	1,380,040.6	$13,800.41	100%
MOD-RWN-	Backfill up to spring line for Rainwater Drainage Network Zone 1	13	15-Dec-25	30-Dec-25	10-Feb-26 A	04-Oct-26	$613,351.42	$12,267.03	100%
MOD-RWN-	Compact layer-wise for Rainwater Drainage Network Zone 1	9	30-Dec-25	10-Jan-26	17-Feb-26 A	04-Oct-26	$460,013.56	$9,200.27	100%
MOD-RWN-	Final fill to subgrade level for Rainwater Drainage Network Zone 1	6	12-Jan-26	18-Jan-26	06-Oct-26	13-Oct-26	$306,675.71	$306,675.71	100%
Gravel Bedding & Filter Cloth for uPVC Drain Pipes		186	02-Nov-25	18-Jan-26	03-Feb-26 A	19-Oct-26	1,529,633.5	$198,852.36	100%
MOD-RWN-	Line trench with filter cloth for Rainwater Drainage Network Zone 1	10	02-Nov-25	13-Nov-25	03-Feb-26 A	03-Oct-26	$152,963.36	$3,059.27	100%
MOD-RWN-	Place and compact gravel bedding for Rainwater Drainage Network Zone 1	12	13-Nov-25	27-Nov-25	09-Feb-26 A	03-Oct-26	$305,926.71	$6,118.53	100%
MOD-RWN-	Lay pipe within gravel zone for Rainwater Drainage Network Zone 1	20	27-Nov-25	21-Dec-25	17-Feb-26 A	03-Oct-26	$688,335.11	$13,766.70	100%
MOD-RWN-	Wrap filter cloth above pipe for Rainwater Drainage Network Zone 1	12	21-Dec-25	04-Jan-26	21-Feb-26 A	05-Oct-26	$229,445.04	$22,944.50	100%
MOD-RWN-	Final fill and trench restoration for Rainwater Drainage Network Zone 1	12	05-Jan-26	18-Jan-26	05-Oct-26	19-Oct-26	$152,963.36	$152,963.36	100%
Potable Water Network Zone 1		360	09-Nov-25	17-Jan-26	10-Sep-25 A	29-Nov-26	2,795,317.1	$374,836.27	100%
Pipe Installation Works		57	09-Nov-25	14-Dec-25	10-Sep-25 A	04-Oct-26	1,603,785.8	$86,203.49	100%
MOD-PWN-PI-	Lean Concrete / Pipe Bedding Preparation for Potable Water Network Zone 1	4	09-Nov-25	12-Nov-25	10-Sep-25 A	03-Oct-26	$100,236.61	$3,007.10	100%
MOD-PWN-PI-	HDPE Pipe Laying (200 mm to 710 mm) for Potable Water Network Zone 1	21	13-Nov-25	03-Dec-25	13-Sep-25 A	03-Oct-26	$902,129.52	$27,063.89	100%
MOD-PWN-PI-	Test (Pressure-slope) for Potable Water Network Zone 1	3	04-Dec-25	06-Dec-25	10-Nov-25 A	03-Oct-26	$200,473.23	$8,018.93	100%
MOD-PWN-PI-	Coating / Wrapping for Potable Water Network Zone 1	5	07-Dec-25	11-Dec-25	04-Nov-25 A	04-Oct-26	$200,473.23	$8,018.93	100%
MOD-PWN-PI-	Backfilling & Warrning Tape for Potable Water Network Zone 1	3	12-Dec-25	14-Dec-25	18-Nov-25 A	04-Oct-26	$200,473.23	$40,094.65	100%
Valve Installation & Chambers		177	09-Nov-25	27-Dec-25	01-Feb-26 A	06-Oct-26	$632,606.85	$89,513.87	100%
MOD-PWN-VC	Gate Valves (225–710 mm) for Potable Water Network Zone 1	12	07-Dec-25	20-Dec-25	14-Feb-26 A	04-Oct-26	$94,891.03	$8,540.19	100%
MOD-PWN-VC	Butterfly Valves (355, 500, 630 mm) for Potable Water Network Zone 1	12	07-Dec-25	20-Dec-25	15-Feb-26 A	04-Oct-26	$75,912.82	$6,832.15	100%
MOD-PWN-VC	3-exit (2 x 2.5-inch and 1 x 4-inch) dry vacuum cylinder detachable fire nozzle for Potabl	12	07-Dec-25	20-Dec-25	14-Feb-26 A	04-Oct-26	$82,238.89	$7,401.50	100%
MOD-PWN-VC	Valve Chamber Excavation for Potable Water Network Zone 1	8	09-Nov-25	17-Nov-25	01-Feb-26 A	03-Oct-26	$158,151.71	$11,070.62	100%
MOD-PWN-VC	RC Slab, Walls, or Precast Chambers for Potable Water Network Zone 1	7	19-Nov-25	26-Nov-25	05-Feb-26 A	04-Oct-26	$126,521.37	$11,386.92	100%
MOD-PWN-VC	Fixing Covers, Gratings, Frames for Potable Water Network Zone 1	4	21-Dec-25	24-Dec-25	24-Mar-26 A	04-Oct-26	$63,260.68	$12,652.14	100%
MOD-PWN-VC	Tagging & Painting for Potable Water Network Zone 1	2	25-Dec-25	27-Dec-25	04-Oct-26	06-Oct-26	$31,630.34	$31,630.34	100%
Flow Meter Installation		140	25-Nov-25	17-Jan-26	07-May-26 A	29-Nov-26	$86,150.62	$78,027.85	100%
MOD-PWN-FM	RC or Precast Chamber Construction for Potable Water Network Zone 1	8	25-Nov-25	03-Dec-25	07-May-26 A	07-Oct-26	$18,460.85	$10,338.07	100%
MOD-PWN-FM	Flowmeter Installation & Pipe Integration for Potable Water Network Zone 1	15	18-Dec-25	04-Jan-26	29-Oct-26	16-Nov-26	$43,075.31	$43,075.31	100%
MOD-PWN-FM	Wiring/Cabling if applicable for Potable Water Network Zone 1	8	05-Jan-26	13-Jan-26	16-Nov-26	25-Nov-26	$18,460.85	$18,460.85	100%
MOD-PWN-FM	Calibration & Commissioning for Potable Water Network Zone 1	3	14-Jan-26	17-Jan-26	25-Nov-26	29-Nov-26	$6,153.62	$6,153.62	100%
Washout & Air Valve Chambers		42	29-Nov-25	06-Jan-26	09-Aug-26 A	13-Oct-26	$472,773.86	$121,091.07	100%
MOD-PWN-WA	Pipe Work for Potable Water Network Zone 1	12	29-Nov-25	11-Dec-25	09-Aug-26 A	04-Oct-26	$175,212.80	$17,521.28	100%
MOD-PWN-WA	Washout (Valve + Outlet) Installation for Potable Water Network Zone 1	8	13-Dec-25	21-Dec-25	16-Aug-26 A	05-Oct-26	$129,538.51	$25,907.70	100%
MOD-PWN-WA	Air Valve Rooms (Valve + Outlet) Installation for Potable Water Network Zone 1	7	22-Dec-25	29-Dec-25	16-Aug-26 A	07-Oct-26	$90,150.20	$27,045.06	100%
MOD-PWN-WA	Covers, Ladders & Tags for Potable Water Network Zone 1	4	30-Dec-25	03-Jan-26	14-Sep-26 A	10-Oct-26	$38,936.18	$11,680.85	100%
MOD-PWN-WA	Backfilling & Final Finishing for Potable Water Network Zone 1	3	04-Jan-26	06-Jan-26	10-Oct-26	13-Oct-26	$38,936.18	$38,936.18	100%

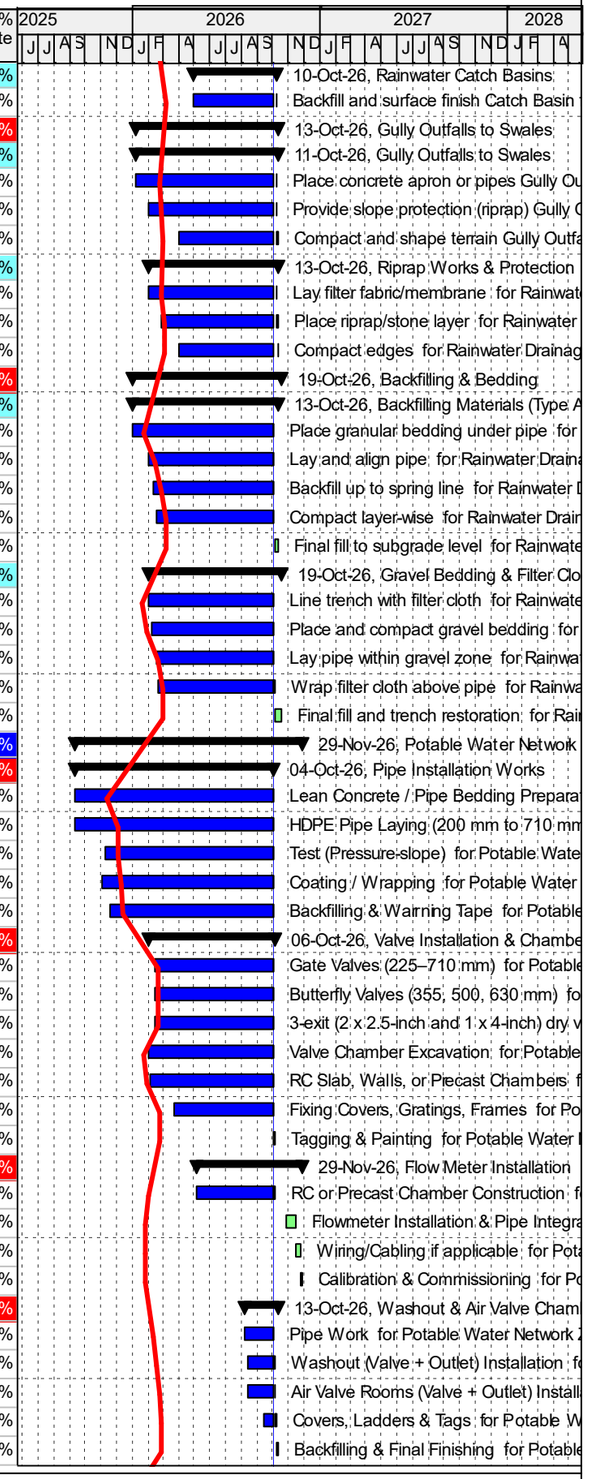


Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary

TASK filter: Schedule %.

© Oracle Corporation

Development of Phase One – Part Two – Third Industrial

Activity ID	Activity Name	Original Duration	BL Project Start	BL Project Finish	Start	Finish	Budgeted Total Cost	Remaining Total Cost	Schedule % Complete
Irrigation Network Zone 1		306	09-Nov-25	18-Jan-26	04-Nov-25 A	09-Nov-26	1,194,399.4	$99,169.00	100%
Excavation, Pipe Laying & Backfilling		101	09-Nov-25	14-Dec-25	04-Nov-25 A	03-Oct-26	$874,055.20	$13,110.83	100%
MOD-IRN-EB-4	Lean Concrete / Pipe Bedding with Type B Material for Irrigation Network Zone 1	9	09-Nov-25	17-Nov-25	04-Nov-25 A	03-Oct-26	$54,628.45	$546.28	100%
MOD-IRN-EB-4	HDPE Pipe Laying (125 mm to 630 mm) for Irrigation Network Zone 1	21	18-Nov-25	08-Dec-25	10-Nov-25 A	03-Oct-26	$491,656.05	$4,916.56	100%
MOD-IRN-EB-4	Test (Pressure-slope) for Irrigation Network Zone 1	2	09-Dec-25	10-Dec-25	01-Jan-26 A	03-Oct-26	$109,256.90	$1,092.57	100%
MOD-IRN-EB-4	Coating / Wrapping for Irrigation Network Zone 1	2	11-Dec-25	12-Dec-25	28-Feb-26 A	03-Oct-26	$109,256.90	$1,092.57	100%
MOD-IRN-EB-4	Backfilling & Warrning Tape for Irrigation Network Zone 1	2	13-Dec-25	14-Dec-25	03-Mar-26 A	03-Oct-26	$109,256.90	$5,462.84	100%
Valves and Appurtenances		79	07-Dec-25	29-Dec-25	01-Feb-26 A	06-Oct-26	$127,197.68	$10,710.04	100%
MOD-IRN-VA-0	Supply & Installation of Valves (Gate Valve) for Irrigation Network Zone 1	8	07-Dec-25	15-Dec-25	01-Feb-26 A	03-Oct-26	$78,843.59	$3,942.18	100%
MOD-IRN-VA-0	Supply & Installation of Valves (Butterfly Valve) for Irrigation Network Zone 1	9	11-Dec-25	21-Dec-25	05-Feb-26 A	03-Oct-26	$35,634.32	$1,781.72	100%
MOD-IRN-VA-0	Installation of Flanges, Bolts, Collars, Nuts for Irrigation Network Zone 1	3	22-Dec-25	24-Dec-25	26-Mar-26 A	03-Oct-26	$5,087.91	$407.03	100%
MOD-IRN-VA-0	Valve Pressure Testing for Irrigation Network Zone 1	2	25-Dec-25	27-Dec-25	05-Jul-26 A	04-Oct-26	$3,179.94	$1,907.97	100%
MOD-IRN-VA-0	Support Brackets/Anchor Blocks for Irrigation Network Zone 1	2	28-Dec-25	29-Dec-25	01-Apr-26 A	06-Oct-26	$4,451.92	$2,671.15	100%
Valve Rooms		26	29-Dec-25	18-Jan-26	01-Mar-26 A	07-Oct-26	$102,251.66	$21,148.05	100%
MOD-IRN-VR-0	Blinding Concrete Valve Chamber for Irrigation Network Zone 1	2	29-Dec-25	30-Dec-25	01-Mar-26 A	03-Oct-26	$12,029.61	$601.48	100%
MOD-IRN-VR-0	RCC Base Slab & Chamber Walls Valve Chamber for Irrigation Network Zone 1	4	31-Dec-25	04-Jan-26	04-Mar-26 A	04-Oct-26	$14,435.53	$2,165.33	100%
MOD-IRN-VR-0	Block Wall Construction (if any) Valve Chamber for Irrigation Network Zone 1	4	05-Jan-26	08-Jan-26	07-Mar-26 A	05-Oct-26	$21,653.29	$4,547.19	100%
MOD-IRN-VR-0	Installation of Valve inside the Room Valve Chamber for Irrigation Network Zone 1	5	10-Jan-26	14-Jan-26	05-Apr-26 A	06-Oct-26	$30,074.02	$6,315.54	100%
MOD-IRN-VR-0	Fixing Frame & Cover Valve Chamber for Irrigation Network Zone 1	2	15-Jan-26	17-Jan-26	11-Jul-26 A	06-Oct-26	$18,044.41	$4,511.10	100%
MOD-IRN-VR-0	Backfilling and Finishing Valve Chamber for Irrigation Network Zone 1	1	18-Jan-26	18-Jan-26	13-Jul-26 A	07-Oct-26	$6,014.80	$3,007.40	100%
Washout Chambers		16	12-Jan-26	18-Jan-26	23-Jun-26 A	03-Oct-26	$28,122.71	$843.68	100%
MOD-IRN-WC-I	Manhole Frame, Cover & Ladder Fixing Washout Chamber for Irrigation Network Zone 1	5	12-Jan-26	17-Jan-26	23-Jun-26 A	03-Oct-26	$21,092.04	$632.76	100%
MOD-IRN-WC-I	Backfilling & Reinstatement Washout Chamber for Irrigation Network Zone 1	1	18-Jan-26	18-Jan-26	04-Jul-26 A	03-Oct-26	$7,030.68	$210.92	100%
Flow Meter Chambers		70	06-Jan-26	18-Jan-26	01-Jul-26 A	09-Nov-26	$62,772.24	$53,356.40	100%
MOD-IRN-FC-0	Flow Meter Installation (280, 300, 500 mm) Flow Meter Chamber for Irrigation Network Zo	6	06-Jan-26	12-Jan-26	01-Jul-26 A	05-Nov-26	$31,386.12	$31,386.12	100%
MOD-IRN-FC-0	Integration with Pipework Flow Meter Chamber for Irrigation Network Zone 1	2	13-Jan-26	14-Jan-26	02-Jul-26 A	05-Nov-26	$13,451.19	$4,035.36	100%
MOD-IRN-FC-0	Testing & Calibration Flow Meter Chamber for Irrigation Network Zone 1	2	15-Jan-26	17-Jan-26	05-Nov-26	08-Nov-26	$13,451.19	$13,451.19	100%
MOD-IRN-FC-0	Cover and Access Arrangement Flow Meter Chamber for Irrigation Network Zone 1	1	18-Jan-26	18-Jan-26	08-Nov-26	09-Nov-26	$4,483.73	$4,483.73	100%
Rainwater Collection Ponds Zone 1		207	05-Feb-26	11-Oct-26	03-Sep-25 A	04-Feb-27	10,360,045.1	$2,651,582.25	98.84%
Excavation for Rainwater Drainage Pond		207	05-Feb-26	14-Mar-26	30-Nov-25 A	09-Jan-27	$111,627.22	$21,987.18	100%
Deep excavation, backfill, disposal for pond formation		207	05-Feb-26	14-Mar-26	30-Nov-25 A	09-Jan-27	$111,627.22	$21,987.18	100%
MOD-RCP-E	Dewater during excavation for Rainwater Collection Ponds Zone 1	5	05-Feb-26	10-Feb-26	30-Nov-25 A	02-Jan-27	$50,739.65	$5,073.96	100%
MOD-RCP-E	Place warning tapes for Rainwater Collection Ponds Zone 1	6	11-Feb-26	19-Feb-26	10-Dec-25 A	03-Jan-27	$12,684.91	$2,536.98	100%
MOD-RCP-E	Dispose of rock/materials to approved dump area for Rainwater Collection Ponds Zone	7	19-Feb-26	05-Mar-26	17-Dec-25 A	04-Jan-27	$42,283.04	$8,456.61	100%
MOD-RCP-E	Backfill selected areas as per design for Rainwater Collection Ponds Zone 1	2	07-Mar-26	10-Mar-26	04-Jan-27	06-Jan-27	$3,382.64	$3,382.64	100%
MOD-RCP-E	Final trimming and profiling for Rainwater Collection Ponds Zone 1	2	10-Mar-26	14-Mar-26	06-Jan-27	09-Jan-27	$2,536.98	$2,536.98	100%
General Site Preparation		42	02-Jul-26	20-Aug-26	08-Dec-25 A	16-Jan-27	9,443,984.2	$2,360,996.07	100%
MOD-RCP-GS-	Earthwork excavation (other than topsoil or rock) - Zone 1 (2 Ponds) - P3	21	02-Jul-26	27-Jul-26	10-Dec-25 A	09-Jan-27	5,126,449.2	$1,281,612.31	100%
MOD-RCP-GS-	Transport and disposal to approved locations - Zone 1 (2 Ponds) - P3	21	27-Jul-26	20-Aug-26	08-Dec-25 A	16-Jan-27	4,317,535.0	$1,079,383.76	100%
Backfilling Works		97	27-Jul-26	06-Oct-26	03-Sep-25 A	23-Jan-27	$343,845.76	$72,388.58	85%
MOD-RCP-BW	Select material from excavation or import approved material for Rainwater Collection Po	15	27-Jul-26	13-Aug-26	03-Sep-25 A	11-Jan-27	$72,388.58	$7,238.86	100%
MOD-RCP-BW	Place in layers not exceeding 300mm for Rainwater Collection Ponds Zone 1	21	13-Aug-26	07-Sep-26	03-Sep-25 A	16-Jan-27	$126,680.02	$25,336.00	100%
MOD-RCP-BW	Compact each layer to required density for Rainwater Collection Ponds Zone 1	20	07-Sep-26	01-Oct-26	16-Nov-25 A	20-Jan-27	$90,485.73	$18,097.15	100%
MOD-RCP-BW	Conduct field density tests for Rainwater Collection Ponds Zone 1	4	01-Oct-26	06-Oct-26	01-Aug-26 A	23-Jan-27	$54,291.44	$21,716.57	5%
Geotextile & Bedding		49	13-Aug-26	11-Oct-26	07-Jan-26 A	04-Feb-27	$460,587.84	$196,210.42	85.14%
Installation of geotextile lining and coarse sand bedding		49	13-Aug-26	11-Oct-26	07-Jan-26 A	04-Feb-27	$460,587.84	$196,210.42	85.14%
MOD-RCP-C	Trim subgrade to required level for Rainwater Collection Ponds Zone 1	7	13-Aug-26	22-Aug-26	07-Jan-26 A	14-Jan-27	$61,411.71	$24,564.68	100%
MOD-RCP-C	Lay HDPE geotextile membrane over compacted soil for Rainwater Collection Ponds Zo	21	22-Aug-26	15-Sep-26	15-Jan-26 A	25-Jan-27	$214,940.99	$92,424.63	100%
MOD-RCP-C	Place 500mm thick coarse sand bedding for Rainwater Collection Ponds Zone 1	21	15-Sep-26	11-Oct-26	22-Jan-26 A	04-Feb-27	$184,235.14	$79,221.11	62.86%
Road Crossing Zone 1		91	22-Jun-26	07-Oct-26	08-Apr-27	27-Jul-27	1,112,631.4	$1,112,631.40	97.84%

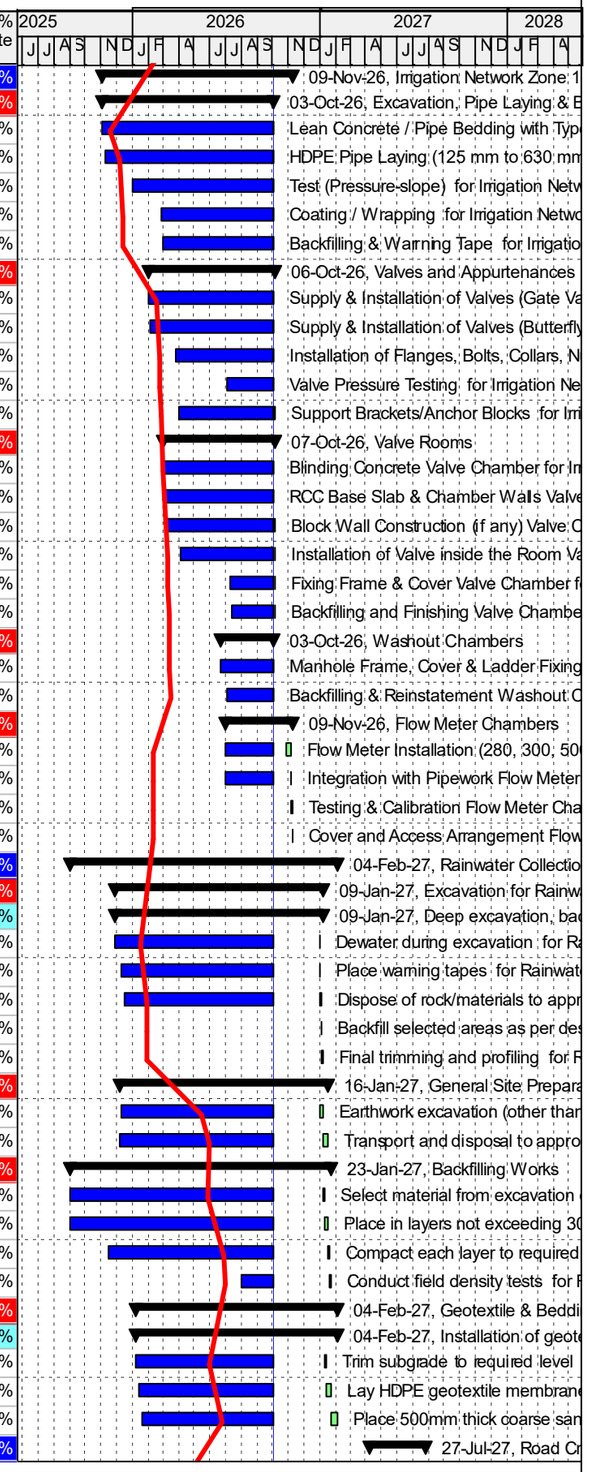


Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary

TASK filter: Schedule %.

© Oracle Corporation

Development of Phase One – Part Two – Third Industrial


Activity ID	Activity Name	Original Duration	BL Project Start	BL Project Finish	Start	Finish	Budgeted Total Cost	Remaining Total Cost	Schedule % Complete
uPVC Road Crossing Pipes		91	22-Jun-26	07-Oct-26	08-Apr-27	27-Jul-27	1,112,631.4(	$1,112,631.40	97.84%
Installation of uPVC pipes of various diameters crossing roadways		91	22-Jun-26	07-Oct-26	08-Apr-27	27-Jul-27	1,112,631.4(	$1,112,631.40	97.84%
MOD-ROC-F	Demarcation and traffic diversion (if required) for Road Crossing Zone 1	6	22-Jun-26	29-Jun-26	08-Apr-27	14-Apr-27	$60,142.24	$60,142.24	100%
MOD-ROC-F	Saw cutting and removal of asphalt (if applicable) for Road Crossing Zone 1	12	29-Jun-26	13-Jul-26	15-Apr-27	28-Apr-27	$120,284.48	$120,284.48	100%
MOD-ROC-F	Excavation across road width to required depth for Road Crossing Zone 1	21	13-Jul-26	06-Aug-26	29-Apr-27	27-May-27	$180,426.71	$180,426.71	100%
MOD-ROC-F	Preparation of trench base with compacted bedding for Road Crossing Zone 1	15	06-Aug-26	24-Aug-26	29-May-27	14-Jun-27	$120,284.48	$120,284.48	100%
MOD-ROC-F	Laying of uPVC pipe (300mm, 315mm, 400mm, 600mm dia) for Road Crossing Zone 1	21	24-Aug-26	17-Sep-26	15-Jun-27	08-Jul-27	$481,137.90	$481,137.90	100%
MOD-ROC-F	Placement of supports and protection around the pipe for Road Crossing Zone 1	10	17-Sep-26	30-Sep-26	10-Jul-27	20-Jul-27	$120,284.48	$120,284.48	100%
MOD-ROC-F	Testing of installed pipeline for Road Crossing Zone 1	6	30-Sep-26	07-Oct-26	21-Jul-27	27-Jul-27	$30,071.12	$30,071.12	20%
General		187	07-May-26	12-Oct-26	04-Nov-25 A	24-May-27	7,330,565.0	$2,069,748.22	96.5%
Local Roads		4	29-Aug-26	02-Sep-26	10-Apr-27	14-Apr-27	$217.04	$217.04	100%
Bituminous Construction		4	29-Aug-26	02-Sep-26	10-Apr-27	14-Apr-27	$217.04	$217.04	100%
Bituminous Foundation Layer (MC 1)		4	29-Aug-26	02-Sep-26	10-Apr-27	14-Apr-27	$217.04	$217.04	100%
MOD-LOR-E	Prepare subgrade for Local Roads	4	29-Aug-26	02-Sep-26	10-Apr-27	14-Apr-27	$217.04	$217.04	100%
Arterial Roads		154	07-May-26	29-Aug-26	27-Jun-26 A	10-Apr-27	$479,616.37	$430,019.33	100%
Earthworks		2	07-May-26	10-May-26	16-Jan-27	18-Jan-27	$16,092.57	$16,092.57	100%
MOD-ARR-EW	Clear vegetation for Arterial Roads	1	07-May-26	09-May-26	16-Jan-27	17-Jan-27	$8,046.29	$8,046.29	100%
MOD-ARR-EW	Site Grading for Arterial Roads	1	09-May-26	10-May-26	17-Jan-27	18-Jan-27	$8,046.29	$8,046.29	100%
Precast Curbs (Type K1-D)		154	10-May-26	29-Aug-26	27-Jun-26 A	10-Apr-27	$463,523.80	$413,926.75	100%
MOD-ARR-PC-I	Excavation & Subgrade Prep for Arterial Roads	8	10-May-26	19-May-26	27-Jun-26 A	25-Jan-27	$46,352.38	$36,154.86	100%
MOD-ARR-PC-I	Concrete Base & Hunching for Arterial Roads	8	19-May-26	02-Jun-26	29-Jun-26 A	02-Feb-27	$46,352.38	$37,081.90	100%
MOD-ARR-PC-I	Curb Installation for Arterial Roads	21	07-Jul-26	01-Aug-26	01-Jul-26 A	08-Mar-27	$231,761.90	$201,632.85	100%
MOD-ARR-PC-I	Backfilling & Compaction for Arterial Roads	8	01-Aug-26	10-Aug-26	08-Mar-27	22-Mar-27	$46,352.38	$46,352.38	100%
MOD-ARR-PC-I	Finishing for Arterial Roads	8	10-Aug-26	19-Aug-26	22-Mar-27	31-Mar-27	$46,352.38	$46,352.38	100%
MOD-ARR-PC-I	Waste Disposal for Arterial Roads	8	19-Aug-26	29-Aug-26	31-Mar-27	10-Apr-27	$46,352.38	$46,352.38	100%
Communications		148	22-Jun-26	12-Oct-26	04-Nov-25 A	07-Apr-27	6,185,396.5	$974,176.71	97.59%
Ductworks		148	22-Jun-26	12-Oct-26	04-Nov-25 A	07-Apr-27	6,185,396.5	$974,176.71	97.59%
Concrete-Protected Service Culverts (50mm, 8 Outlets)		148	22-Jun-26	16-Sep-26	04-Nov-25 A	05-Apr-27	5,830,115.7	$938,648.63	100%
MOD-COC-I	Trench Excavation for Communications	10	22-Jun-26	08-Jul-26	04-Nov-25 A	24-Feb-27	1,749,034.7	$69,961.39	100%
MOD-COC-I	Culvert Installation & Concrete Protection for Communications	18	08-Jul-26	29-Jul-26	08-Nov-25 A	28-Feb-27	2,915,057.8	$204,054.05	100%
MOD-COC-I	Backfilling & Compaction for Communications	21	29-Jul-26	23-Aug-26	10-Nov-25 A	04-Mar-27	$583,011.57	$81,621.62	100%
MOD-COC-I	Testing & Restoration for Communications	21	23-Aug-26	16-Sep-26	06-Mar-27	05-Apr-27	$583,011.57	$583,011.57	100%
Road Crossing Ducts (Exit 8)		21	16-Sep-26	12-Oct-26	01-Dec-25 A	07-Apr-27	$355,280.83	$35,528.08	58.1%
MOD-COC-I	Horizontal Directional Drilling (HDD) for Communications	21	16-Sep-26	12-Oct-26	01-Dec-25 A	07-Apr-27	$355,280.83	$35,528.08	58.1%
Landscape		62	29-Jul-26	11-Oct-26	28-Feb-27	24-May-27	$665,335.14	$665,335.14	83.85%
Supply & Planting of Trees and Shrubs		45	18-Aug-26	11-Oct-26	28-Mar-27	24-May-27	$578,701.17	$578,701.17	81.43%
planting of trees, shrubs, and vines		45	18-Aug-26	11-Oct-26	28-Mar-27	24-May-27	$578,701.17	$578,701.17	81.43%
MOD-LNS-F	Site demarcation and marking of plant locations for Landscape	8	18-Aug-26	27-Aug-26	28-Mar-27	06-Apr-27	$96,450.19	$96,450.19	100%
MOD-LNS-F	Excavation of planting pits as per specification for Landscape	16	27-Aug-26	15-Sep-26	06-Apr-27	25-Apr-27	$192,900.39	$192,900.39	100%
MOD-LNS-F	Placement of sweet soil/potting soil as required for Landscape	21	15-Sep-26	11-Oct-26	25-Apr-27	24-May-27	$289,350.58	$289,350.58	62.86%
Gravel Layer and Bed Preparation		37	29-Jul-26	10-Sep-26	28-Feb-27	20-Apr-27	$86,633.98	$86,633.98	100%
Installation of gravel layers and soil beds to support planting and drainage.		37	29-Jul-26	10-Sep-26	28-Feb-27	20-Apr-27	$86,633.98	$86,633.98	100%
MOD-LNS-C	Grading of planting areas for Landscape	2	29-Jul-26	01-Aug-26	28-Feb-27	03-Mar-27	$4,331.70	$4,331.70	100%
MOD-LNS-C	Excavation to required depth for Landscape	5	01-Aug-26	06-Aug-26	03-Mar-27	16-Mar-27	$8,663.40	$8,663.40	100%
MOD-LNS-C	Placement of 50mm gravel layer for green areas for Landscape	10	06-Aug-26	18-Aug-26	16-Mar-27	28-Mar-27	$25,990.19	$25,990.19	100%
MOD-LNS-C	Placement of 150mm gravel bed for drainage network for Landscape	6	18-Aug-26	25-Aug-26	28-Mar-27	04-Apr-27	$12,995.10	$12,995.10	100%
MOD-LNS-C	Spreading and compacting the gravel for Landscape	6	25-Aug-26	01-Sep-26	04-Apr-27	11-Apr-27	$12,995.10	$12,995.10	100%
MOD-LNS-C	Overlay of semi-permeable membrane (if applicable) for Landscape	4	01-Sep-26	06-Sep-26	11-Apr-27	15-Apr-27	$10,829.25	$10,829.25	100%
MOD-LNS-C	Spreading of potting soil/sweet soil as top layer for Landscape	4	06-Sep-26	10-Sep-26	15-Apr-27	20-Apr-27	$10,829.25	$10,829.25	100%
Testing & Commissioning & Closeout		95	12-Jan-26	09-Apr-26	14-Jan-26 A	26-Dec-26	14,456,186.2	$4,047,732.15	100%

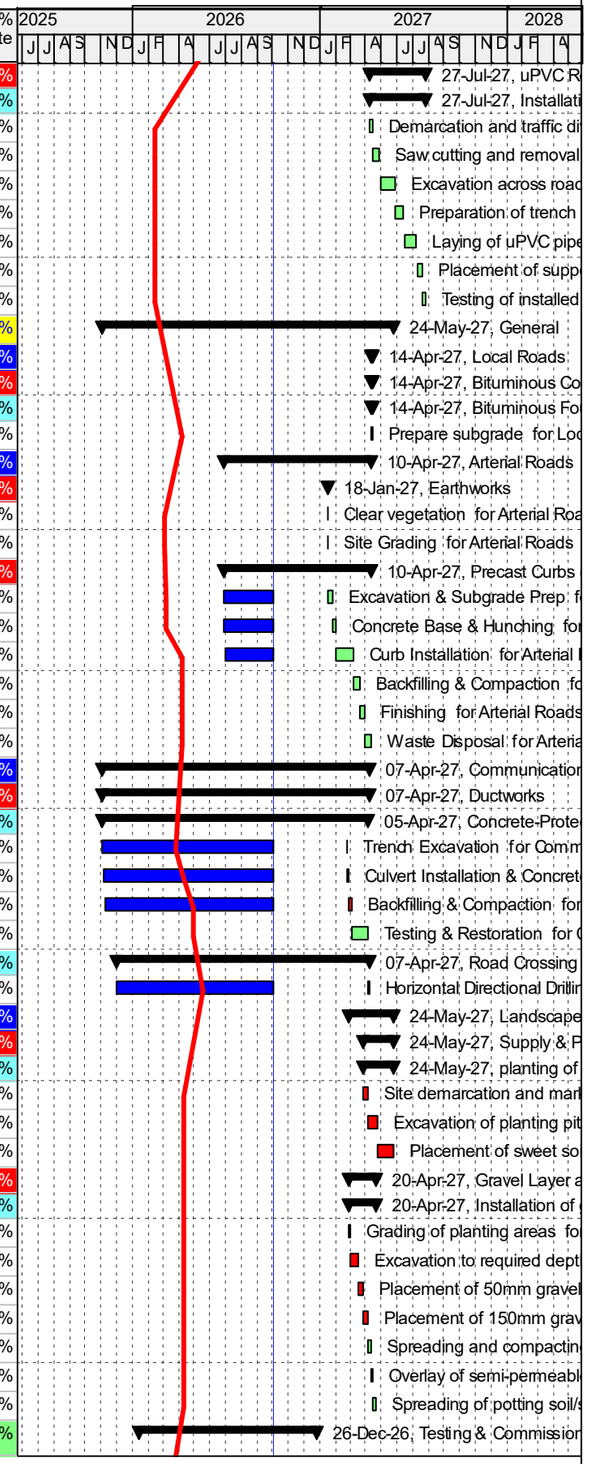

© Oracle Corporation

Development of Phase One – Part Two – Third Industrial

Activity ID	Activity Name	Original Duration	BL Project Start	BL Project Finish	Start	Finish	Budgeted Total Cost	Remaining Total Cost	Schedule % Complete
Testing & Commissioning		95	12-Jan-26	09-Apr-26	14-Jan-26 A	26-Dec-26	14,456,186.2	$4,047,732.15	100%
Zone 3		77	12-Jan-26	09-Apr-26	20-Jan-26 A	20-Dec-26	2,891,237.2	$578,247.45	100%
A102060	Testing and Commissioning for Sewerage Network Zone 3	21	05-Mar-26	09-Apr-26	05-Mar-26 A	20-Dec-26	$350,278.50	$70,055.70	100%
A103590	Testing and Commissioning for Rain Water Drainage Network Zone 3	21	19-Jan-26	11-Feb-26	29-Jan-26 A	01-Dec-26	1,789,001.6	$357,800.33	100%
A103600	Testing and Commissioning for Potable Water Network Zone 3	21	19-Jan-26	11-Feb-26	31-Jan-26 A	28-Nov-26	$454,067.96	$90,813.59	100%
A103610	Testing and Commissioning for Irrigation Network Zone 3	21	12-Jan-26	04-Feb-26	20-Jan-26 A	13-Dec-26	$297,889.13	$59,577.83	100%
Zone 2		84	14-Jan-26	09-Apr-26	14-Jan-26 A	15-Dec-26	5,782,474.4	$1,734,742.35	100%
A103640	Testing and Commissioning for Sewerage Network Zone 2	21	05-Mar-26	09-Apr-26	05-Mar-26 A	15-Dec-26	$700,557.00	$210,167.10	100%
A103650	Testing and Commissioning for Rain Water Drainage Network Zone 2	21	19-Jan-26	11-Feb-26	11-Apr-26 A	17-Nov-26	3,578,003.3	$1,073,401.00	100%
A103660	Testing and Commissioning for Potable Water Network Zone 2	21	14-Jan-26	07-Feb-26	14-Jan-26 A	02-Dec-26	$908,135.90	$272,440.77	100%
A103670	Testing and Commissioning for Irrigation Network Zone 2	21	19-Jan-26	11-Feb-26	10-Feb-26 A	15-Nov-26	$595,778.27	$178,733.48	100%
Zone 1		86	18-Jan-26	25-Mar-26	18-Jan-26 A	26-Dec-26	5,782,474.4	$1,734,742.35	100%
A103690	Testing and Commissioning for Sewerage Network Zone 1	21	11-Feb-26	25-Mar-26	11-Feb-26 A	26-Dec-26	$700,557.00	$210,167.10	100%
A103700	Testing and Commissioning for Rain Water Drainage Network Zone 1	21	19-Jan-26	11-Feb-26	19-Jan-26 A	09-Nov-26	3,578,003.3	$1,073,401.00	100%
A103710	Testing and Commissioning for Potable Water Network Zone 1	21	18-Jan-26	10-Feb-26	18-Jan-26 A	06-Dec-26	$908,135.90	$272,440.77	100%
A103720	Testing and Commissioning for Irrigation Network Zone 1	21	19-Jan-26	11-Feb-26	19-Jan-26 A	17-Nov-26	$595,778.27	$178,733.48	100%

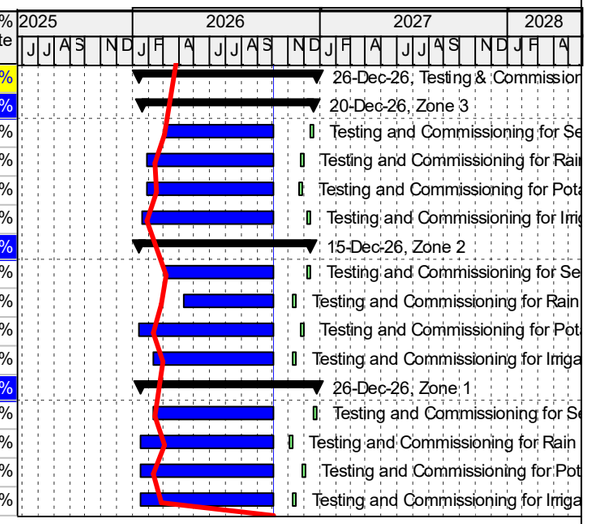

© Oracle Corporation
