
Development of Phase One – Part Two – Third Industrial

Activity ID	Activity Name	Original Duration	BL Project Start	BL Project Finish	Start	Finish	Budgeted Total Cost	Remaining Total Cost	Schedule % Complete
Development of Phase One – Part Two – Third Industrial City in Dammam - 01-C		370	19-May-25	25-Oct-26	01-Jul-26 A	27-Jul-27	,274,910.77	$23,274,910.77	96.45%
Milestones		90	16-Jul-25	18-Jan-26	03-Oct-26	31-Dec-26	$0.00	$0.00	0%
MIL-0006	Completion of Rainwater Drainage Works	0		18-Jan-26		31-Dec-26*	$0.00	$0.00	100%
MIL-0005	Completion of Water Networks and Tanks	0		18-Jan-26		31-Dec-26*	$0.00	$0.00	100%
MIL-0004	Submission and Approval of Drawings and Specifications	0		16-Jul-25		08-Oct-26*	$0.00	$0.00	100%
MIL-0003	Submission of Report, Work Plan, and Schedule	0		17-Jul-25		03-Oct-26	$0.00	$0.00	100%
Mobilization		70	19-May-25	13-Aug-25	03-Oct-26	22-Dec-26	$0.00	$0.00	0%
Deliverables		70	19-May-25	13-Aug-25	03-Oct-26	22-Dec-26	$0.00	$0.00	0%
Submittals		60	19-May-25	02-Aug-25	03-Oct-26	10-Dec-26	$0.00	$0.00	0%
S100015	Prepare & Submit Pre-commissioning/ Commissioning Plan/ Startup/ Testing / Handover	60	19-May-25	02-Aug-25	03-Oct-26	10-Dec-26	$0.00	$0.00	100%
Approvals		10	03-Aug-25	13-Aug-25	12-Dec-26	22-Dec-26	$0.00	$0.00	0%
S100086	Approval of Pre-commissioning/ Commissioning Plan/ Startup/ Testing / Handover Plan	10	03-Aug-25	13-Aug-25	12-Dec-26	22-Dec-26	$0.00	$0.00	100%
Procurement		94	03-Mar-26	31-Aug-26	14-Oct-26	01-Feb-27	1,615,201.5	$1,615,201.56	100%
Long Lead Items		30	27-Jul-26	31-Aug-26	26-Oct-26	30-Nov-26	$0.00	$0.00	0%
Odor Control Units - Sewer PS-specific		30	27-Jul-26	31-Aug-26	26-Oct-26	30-Nov-26	$0.00	$0.00	0%
A102720	Staging Time for Odor Control Units - Sewer PS-specific	30	27-Jul-26	31-Aug-26	26-Oct-26	30-Nov-26	$0.00	$0.00	100%
Short Lead Items		94	03-Mar-26	07-Jul-26	14-Oct-26	01-Feb-27	1,615,201.5	$1,615,201.56	100%
Landscaping Materials (Soil, Plants) - Final works, softscape		94	03-Mar-26	07-Jul-26	14-Oct-26	01-Feb-27	1,615,201.5	$1,615,201.56	100%
A102390	Delivery for Landscaping Materials (Soil, Plants) - Final works, softscape	30	02-Jun-26	07-Jul-26	28-Dec-26	01-Feb-27	1,615,201.5	$1,615,201.56	100%
A102360	Manufacturing for Landscaping Materials (Soil, Plants) - Final works, softscape	60	11-Mar-26	02-Jun-26	19-Oct-26	28-Dec-26	$0.00	$0.00	100%
A102350	Issue PO for Landscaping Materials (Soil, Plants) - Final works, softscape	4	03-Mar-26	10-Mar-26	14-Oct-26	19-Oct-26	$0.00	$0.00	100%
Construction		370	19-Oct-25	25-Oct-26	01-Jul-26 A	27-Jul-27	21,659,709.2	$21,659,709.22	96.18%
Zone 3		265	19-Oct-25	07-Oct-26	03-Oct-26	24-Jun-27	11,774,505.3	$11,774,505.34	99.94%
Sewerage Network Zone 3		194	06-Nov-25	10-Jun-26	03-Oct-26	15-Apr-27	3,817,701.7	$3,817,701.75	100%
Pipework: Supply, Installation, and Testing		15	13-Jan-26	27-Jan-26	12-Oct-26	26-Oct-26	$10,418.36	$10,418.36	100%
HDPE Pressure Pipes Installation (250mm–630mm)		15	13-Jan-26	27-Jan-26	12-Oct-26	26-Oct-26	$10,418.36	$10,418.36	100%
MOD-SWN-	Backfilling & Warning Tape HDPE for Sewerage Network Zone 3	15	13-Jan-26	27-Jan-26	12-Oct-26	26-Oct-26	$10,418.36	$10,418.36	100%
Fittings and Valves		27	14-Dec-25	13-Jan-26	03-Oct-26	02-Nov-26	$30,711.20	$30,711.20	100%
MOD-SWN-FV-	Jointing & Piping Accessories Installation for Sewerage Network Zone 3	3	11-Jan-26	13-Jan-26	31-Oct-26	02-Nov-26	$3,071.12	$3,071.12	100%
MOD-SWN-FV-	Air Breather & Air Release Valves Installation for Sewerage Network Zone 3	10	30-Dec-25	10-Jan-26	19-Oct-26	29-Oct-26	$11,590.74	$11,590.74	100%
MOD-SWN-FV-	Drain Valves Installation for Sewerage Network Zone 3	4	25-Dec-25	29-Dec-25	14-Oct-26	18-Oct-26	$4,392.82	$4,392.82	100%
MOD-SWN-FV-	Gate Valves Installation for Sewerage Network Zone 3	4	21-Dec-25	24-Dec-25	10-Oct-26	13-Oct-26	$4,830.30	$4,830.30	100%
MOD-SWN-FV-	Supply & Installation of HDPE Elbows for Sewerage Network Zone 3	6	14-Dec-25	20-Dec-25	03-Oct-26	08-Oct-26	$6,826.21	$6,826.21	100%
Valve & Flow Meter Chambers		44	21-Dec-25	10-Feb-26	01-Nov-26	14-Dec-26	$16,534.51	$16,534.51	100%
Valve Chambers Construction		15	21-Dec-25	04-Jan-26	01-Nov-26	16-Nov-26	$1,378.81	$1,378.81	100%
MOD-SWN-	Backfilling Valve Chamber for Sewerage Network Zone 3	15	21-Dec-25	04-Jan-26	01-Nov-26	16-Nov-26	$1,378.81	$1,378.81	100%
Water Drain Chambers Construction		30	25-Dec-25	23-Jan-26	03-Nov-26	03-Dec-26	$6,718.28	$6,718.28	100%
MOD-SWN-	Test Water Drain Chamber for Sewerage Network Zone 3	15	25-Dec-25	08-Jan-26	03-Nov-26	18-Nov-26	$2,239.43	$2,239.43	100%
MOD-SWN-	Backfilling Water Drain Chamber for Sewerage Network Zone 3	15	09-Jan-26	23-Jan-26	18-Nov-26	03-Dec-26	$4,478.86	$4,478.86	100%
Discharge Chambers Construction		30	07-Jan-26	05-Feb-26	09-Nov-26	09-Dec-26	$4,693.08	$4,693.08	100%
MOD-SWN-	Test Discharge Chamber for Sewerage Network Zone 3	15	07-Jan-26	21-Jan-26	09-Nov-26	24-Nov-26	$1,564.36	$1,564.36	100%
MOD-SWN-	Backfilling Discharge Chamber for Sewerage Network Zone 3	15	22-Jan-26	05-Feb-26	24-Nov-26	09-Dec-26	$3,128.72	$3,128.72	100%
Flow Meter Chambers Construction		35	07-Jan-26	10-Feb-26	09-Nov-26	14-Dec-26	$3,744.33	$3,744.33	100%
MOD-SWN-	Flow Meter Chambers Construction Flow Meter Chamber for Sewerage Network Zone 3	5	07-Jan-26	11-Jan-26	09-Nov-26	14-Nov-26	$2,246.60	$2,246.60	100%
MOD-SWN-	Test Flow Meter Chamber for Sewerage Network Zone 3	15	12-Jan-26	26-Jan-26	14-Nov-26	29-Nov-26	$499.24	$499.24	100%
MOD-SWN-	Backfilling Flow Meter Chamber for Sewerage Network Zone 3	15	27-Jan-26	10-Feb-26	29-Nov-26	14-Dec-26	$998.49	$998.49	100%
Manholes		43	11-Jan-26	04-Mar-26	21-Oct-26	03-Dec-26	$130,812.55	$130,812.55	100%
1500mm GRP Manholes (Standard & Backdrop)		30	11-Jan-26	09-Feb-26	21-Oct-26	20-Nov-26	$120,079.46	$120,079.46	100%
MOD-SWN-	Test 1.5m GRP for Sewerage Network Zone 3	15	11-Jan-26	25-Jan-26	21-Oct-26	05-Nov-26	$40,026.49	$40,026.49	100%

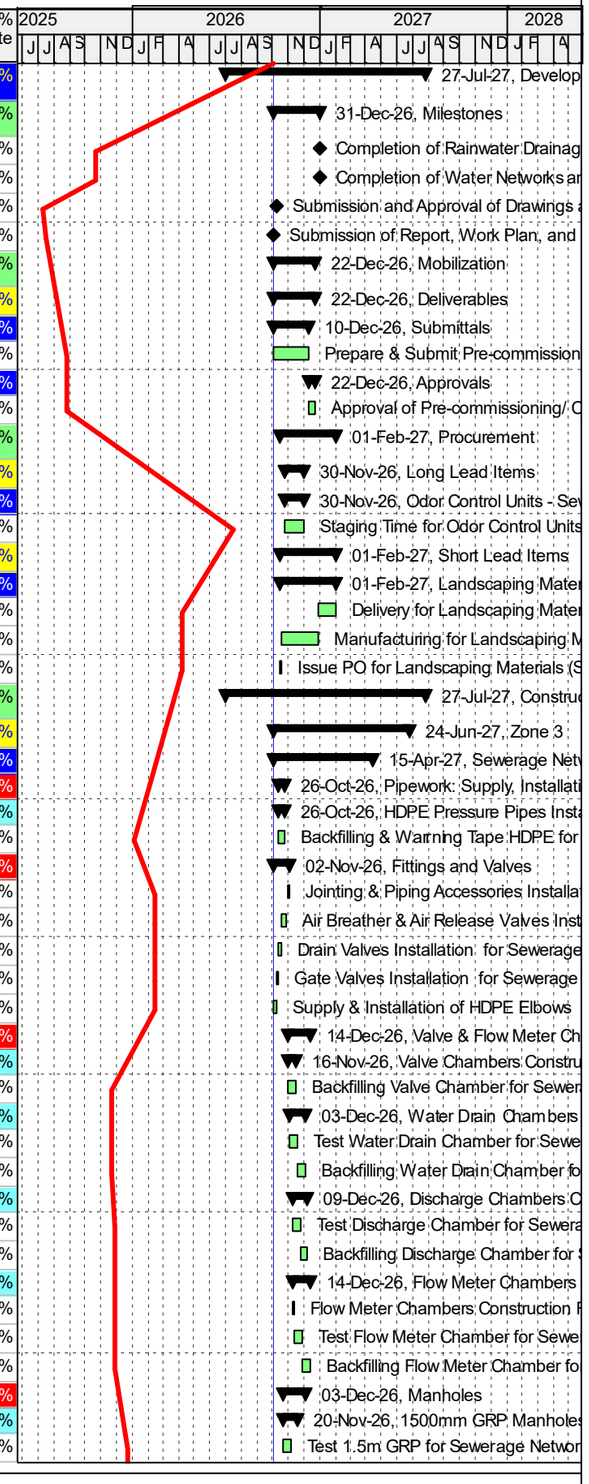


Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary

TASK filter: Activity % (Failed Start).

© Oracle Corporation

Development of Phase One – Part Two – Third Industrial

Activity ID	Activity Name	Original Duration	BL Project Start	BL Project Finish	Start	Finish	Budgeted Total Cost	Remaining Total Cost	Schedule % Complete
MOD-SWN-	Backfilling 1.5m GRP for Sewerage Network Zone 3	15	26-Jan-26	09-Feb-26	05-Nov-26	20-Nov-26	$80,052.97	$80,052.97	100%
1800mm GRP Manholes (Standard & Backdrop)		30	28-Jan-26	26-Feb-26	28-Oct-26	27-Nov-26	$5,990.45	$5,990.45	100%
MOD-SWN-	Test 1.8m GRP for Sewerage Network Zone 3	15	28-Jan-26	11-Feb-26	28-Oct-26	12-Nov-26	$1,996.82	$1,996.82	100%
MOD-SWN-	Backfilling 1.8m GRP for Sewerage Network Zone 3	15	12-Feb-26	26-Feb-26	12-Nov-26	27-Nov-26	$3,993.63	$3,993.63	100%
2000mm GRP Manholes (Standard & Backdrop)		36	28-Jan-26	04-Mar-26	28-Oct-26	03-Dec-26	$4,742.64	$4,742.64	100%
MOD-SWN-	Test 2m GRP for Sewerage Network Zone 3	15	03-Feb-26	17-Feb-26	03-Nov-26	18-Nov-26	$632.35	$632.35	100%
MOD-SWN-	Backfilling 2m GRP for Sewerage Network Zone 3	15	18-Feb-26	04-Mar-26	18-Nov-26	03-Dec-26	$1,264.70	$1,264.70	100%
MOD-SWN-	2000mm GRP Manholes (Standard & Backdrop) 2m GRP for Sewerage Network Zone 3	6	28-Jan-26	02-Feb-26	28-Oct-26	03-Nov-26	$2,845.59	$2,845.59	100%
Pumping Stations		152	06-Nov-25	10-Jun-26	03-Oct-26	15-Apr-27	3,629,225.1	$3,629,225.13	100%
In-Line Booster Stations		63	01-Dec-25	11-Feb-26	03-Oct-26	14-Dec-26	1,968,220.0	$1,968,220.09	100%
MOD-SWN-	In-Line Booster Stations - Civil Works for Sewerage Network Zone 3	21	01-Dec-25	24-Dec-25	03-Oct-26	26-Oct-26	$656,073.36	$656,073.36	100%
MOD-SWN-	In-Line Booster Stations - Electrical Works for Sewerage Network Zone 3	21	19-Jan-26	11-Feb-26	21-Nov-26	14-Dec-26	$656,073.36	$656,073.36	100%
MOD-SWN-	In-Line Booster Stations - Mechanical Works for Sewerage Network Zone 3	21	25-Dec-25	18-Jan-26	27-Oct-26	19-Nov-26	$656,073.36	$656,073.36	100%
Engine/Motor Control Center Buildings		8	06-Nov-25	08-Dec-25	03-Oct-26	11-Oct-26	$45,941.19	$45,941.19	100%
MOD-SWN-	MCC Building – PS4 for Sewerage Network Zone 3	7	01-Dec-25	08-Dec-25	04-Oct-26	11-Oct-26	$42,052.73	$42,052.73	100%
MOD-SWN-	MCC Building – PS3 for Sewerage Network Zone 3	1	06-Nov-25	06-Nov-25	03-Oct-26	03-Oct-26	$3,888.46	$3,888.46	100%
Tank with Canopy		12	28-Dec-25	10-Jan-26	05-Nov-26	19-Nov-26	$720,080.25	$720,080.25	100%
MOD-SWN-	Tank with canopy (per specs/drawings) - PS4 for Sewerage Network Zone 3	12	28-Dec-25	10-Jan-26	05-Nov-26	19-Nov-26	$720,080.25	$720,080.25	100%
Pump Well and Valve Chambers		77	11-Jan-26	14-May-26	19-Nov-26	27-Feb-27	$773,616.05	$773,616.05	100%
MOD-SWN-	Flow meter chamber – PS4 for Sewerage Network Zone 3	13	13-Apr-26	28-Apr-26	02-Feb-27	27-Feb-27	$73,644.14	$73,644.14	100%
MOD-SWN-	Valve chamber – PS4 for Sewerage Network Zone 3	21	12-Mar-26	13-Apr-26	09-Jan-27	02-Feb-27	$124,372.20	$124,372.20	100%
MOD-SWN-	Pump well & valve chamber structure – PS4 (1 well, 4m, 11m depth) for Sewerage Netw	22	04-Feb-26	11-Mar-26	14-Dec-26	09-Jan-27	$129,464.76	$129,464.76	100%
MOD-SWN-	Flow meter chamber – PS3 for Sewerage Network Zone 3	9	04-May-26	14-May-26	11-Jan-27	21-Jan-27	$54,872.10	$54,872.10	100%
MOD-SWN-	Valve chamber – PS3 for Sewerage Network Zone 3	20	11-Apr-26	04-May-26	19-Dec-26	11-Jan-27	$117,056.19	$117,056.19	100%
MOD-SWN-	Concrete wall (5x5x1m) inside PS3 well for Sewerage Network Zone 3	4	06-Apr-26	11-Apr-26	14-Dec-26	19-Dec-26	$19,816.65	$19,816.65	100%
MOD-SWN-	Pump well & valve chamber structure – PS3 (2 wells, 5x5m, 11m depth) for Sewerage N	21	11-Jan-26	03-Feb-26	19-Nov-26	14-Dec-26	$254,390.01	$254,390.01	100%
Odor Control System Base/Plinth		6	03-Jun-26	10-Jun-26	08-Apr-27	15-Apr-27	$16,590.51	$16,590.51	100%
MOD-SWN-	Concrete plinth below odor control – PS3 & PS4 for Sewerage Network Zone 3	6	03-Jun-26	10-Jun-26	08-Apr-27	15-Apr-27	$16,590.51	$16,590.51	100%
Duct Works		7	28-Apr-26	06-May-26	27-Feb-27	16-Mar-27	$15,220.07	$15,220.07	100%
MOD-SWN-	uPVC duct Track 8 – PS3 & PS4 for Sewerage Network Zone 3	4	02-May-26	06-May-26	04-Mar-27	16-Mar-27	$9,274.58	$9,274.58	100%
MOD-SWN-	uPVC duct Track 2 – PS3 & PS4 for Sewerage Network Zone 3	2	29-Apr-26	02-May-26	28-Feb-27	04-Mar-27	$3,185.08	$3,185.08	100%
MOD-SWN-	uPVC duct Track 1 – PS3 & PS4 for Sewerage Network Zone 3	1	28-Apr-26	29-Apr-26	27-Feb-27	28-Feb-27	$2,760.41	$2,760.41	100%
Grounding Works		3	06-May-26	10-May-26	16-Mar-27	20-Mar-27	$7,603.32	$7,603.32	100%
MOD-SWN-	600x600 Cable pull pit – PS3 & PS4 for Sewerage Network Zone 3	2	07-May-26	10-May-26	17-Mar-27	20-Mar-27	$5,913.15	$5,913.15	100%
MOD-SWN-	Grounding pit – PS3 & PS4 for Sewerage Network Zone 3	1	06-May-26	07-May-26	16-Mar-27	17-Mar-27	$1,690.17	$1,690.17	100%
Landscaping / Interlocking Tiles		21	10-May-26	08-Jun-26	20-Mar-27	13-Apr-27	$61,674.68	$61,674.68	100%
MOD-SWN-	Entrance road paving tiles for Sewerage Network Zone 3	4	03-Jun-26	08-Jun-26	08-Apr-27	13-Apr-27	$10,721.87	$10,721.87	100%
MOD-SWN-	Building perimeter interlock tiles for Sewerage Network Zone 3	17	10-May-26	03-Jun-26	20-Mar-27	08-Apr-27	$50,952.81	$50,952.81	100%
Pumping Station Internal Drainage Network		7	10-May-26	18-May-26	20-Mar-27	28-Mar-27	$20,278.98	$20,278.98	100%
MOD-SWN-	Internal surface drainage channels for Sewerage Network Zone 3	7	10-May-26	18-May-26	20-Mar-27	28-Mar-27	$20,278.98	$20,278.98	100%
Rainwater Drainage Network Zone 3		51	02-Dec-25	18-Jan-26	06-Oct-26	26-Nov-26	1,620,343.8	$1,620,343.83	100%
Pipe Laying Works		26	11-Dec-25	05-Jan-26	06-Oct-26	01-Nov-26	$12,638.57	$12,638.57	100%
uPVC Connection Pipes (150mm dia)		26	11-Dec-25	05-Jan-26	06-Oct-26	01-Nov-26	$12,638.57	$12,638.57	100%
MOD-RWN-	Coating / Wrapping UPVC Con. for Rainwater Drainage Network Zone 3	21	14-Dec-25	03-Jan-26	09-Oct-26	30-Oct-26	$4,212.86	$4,212.86	100%
MOD-RWN-	Backfilling & compaction UPVC Con. for Rainwater Drainage Network Zone 3	2	04-Jan-26	05-Jan-26	30-Oct-26	01-Nov-26	$4,212.86	$4,212.86	100%
MOD-RWN-	Test (Pressure-slope) UPVC Con. for Rainwater Drainage Network Zone 3	3	11-Dec-25	13-Dec-25	06-Oct-26	09-Oct-26	$4,212.86	$4,212.86	100%
Precast Concrete Box Culverts		40	02-Dec-25	18-Jan-26	11-Oct-26	26-Nov-26	$556,518.43	$556,518.43	100%
Box Culverts (500x500mm to 3500x800mm)		40	02-Dec-25	18-Jan-26	11-Oct-26	26-Nov-26	$556,518.43	$556,518.43	100%
MOD-RWN-	Surface finishing Box culvert for Rainwater Drainage Network Zone 3	3	14-Jan-26	18-Jan-26	23-Nov-26	26-Nov-26	$31,801.05	$31,801.05	100%
MOD-RWN-	Backfilling and compaction Box culvert for Rainwater Drainage Network Zone 3	7	06-Jan-26	14-Jan-26	15-Nov-26	23-Nov-26	$37,101.23	$37,101.23	100%

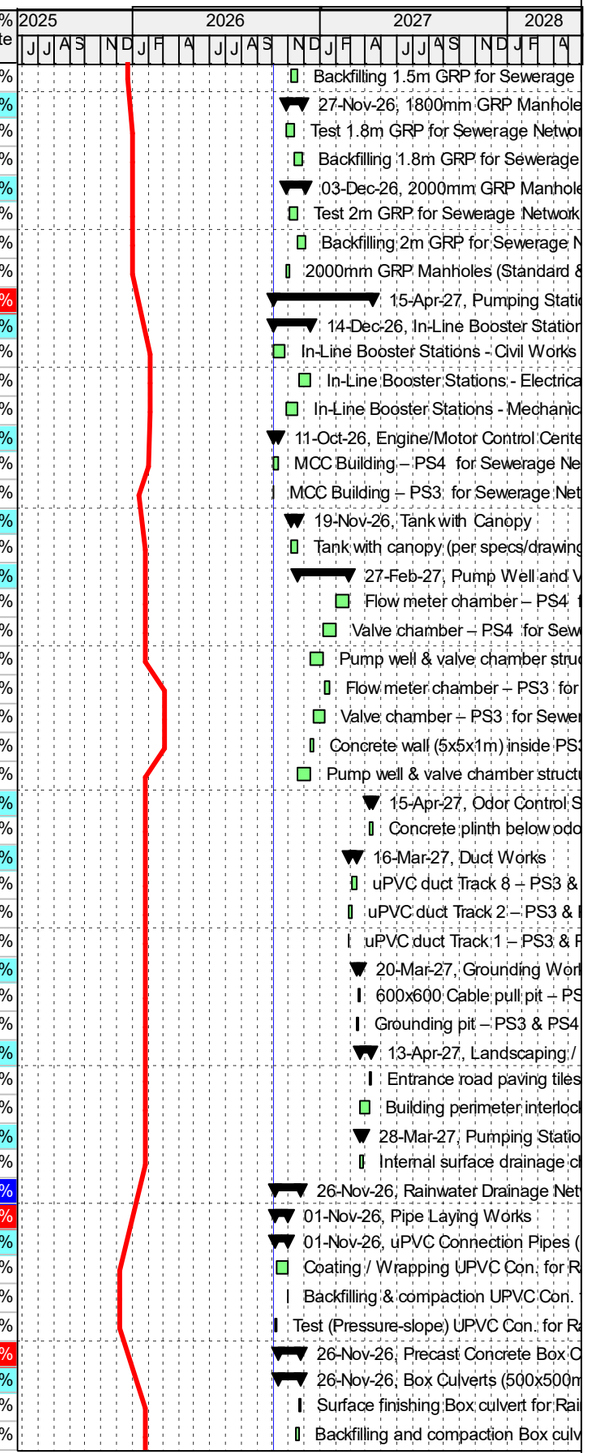


Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary

TASK filter: Activity % (Faiiled Start).

© Oracle Corporation

Development of Phase One – Part Two – Third Industrial

Activity ID	Activity Name	Original Duration	BL Project Start	BL Project Finish	Start	Finish	Budgeted Total Cost	Remaining Total Cost	Schedule % Complete
MOD-RWN-	Construct headwalls/wing walls (if needed) Box culvert for Rainwater Drainage Network Z	12	23-Dec-25	06-Jan-26	01-Nov-26	15-Nov-26	$53,001.76	$53,001.76	100%
MOD-RWN-	Alignment and joint sealing Box culvert for Rainwater Drainage Network Zone 3	4	18-Dec-25	23-Dec-25	27-Oct-26	01-Nov-26	$37,101.23	$37,101.23	100%
MOD-RWN-	Installation of box culvert units Box culvert for Rainwater Drainage Network Zone 3	10	07-Dec-25	18-Dec-25	15-Oct-26	27-Oct-26	$318,010.53	$318,010.53	100%
MOD-RWN-	Bedding preparation (gravel/lean concrete) Box culvert for Rainwater Drainage Network Z	4	02-Dec-25	07-Dec-25	11-Oct-26	15-Oct-26	$79,502.63	$79,502.63	100%
Manholes		36	07-Dec-25	18-Jan-26	15-Oct-26	26-Nov-26	$780,038.12	$780,038.12	100%
Circular GRP Manholes (1200–1800mm dia)		32	07-Dec-25	13-Jan-26	15-Oct-26	22-Nov-26	$228,708.76	$228,708.76	100%
MOD-RWN-	Backfilling and compaction Circular Manhole for Rainwater Drainage Network Zone 3	2	11-Jan-26	13-Jan-26	19-Nov-26	22-Nov-26	$3,430.63	$3,430.63	100%
MOD-RWN-	Waterproofing Circular Manhole for Rainwater Drainage Network Zone 3	2	08-Jan-26	11-Jan-26	17-Nov-26	19-Nov-26	$4,574.18	$4,574.18	100%
MOD-RWN-	Place slab and cover frame Circular Manhole for Rainwater Drainage Network Zone 3	6	01-Jan-26	08-Jan-26	10-Nov-26	17-Nov-26	$17,153.16	$17,153.16	100%
MOD-RWN-	Install GRP manhole shaft sections Circular Manhole for Rainwater Drainage Network Zo	7	24-Dec-25	01-Jan-26	02-Nov-26	10-Nov-26	$57,177.19	$57,177.19	100%
MOD-RWN-	Concrete base construction Circular Manhole for Rainwater Drainage Network Zone 3	2	22-Dec-25	24-Dec-25	31-Oct-26	02-Nov-26	$68,612.63	$68,612.63	100%
MOD-RWN-	Dewatering and safety barriers Circular Manhole for Rainwater Drainage Network Zone 3	6	15-Dec-25	22-Dec-25	24-Oct-26	31-Oct-26	$69,756.17	$69,756.17	100%
MOD-RWN-	Excavate to full manhole depth Circular Manhole for Rainwater Drainage Network Zone 3	7	07-Dec-25	15-Dec-25	15-Oct-26	24-Oct-26	$8,004.81	$8,004.81	100%
Concrete Manholes for 1500x1500 Box Pipes		32	07-Dec-25	13-Jan-26	15-Oct-26	22-Nov-26	$354,504.29	$354,504.29	100%
MOD-RWN-	Backfill in layers Concrete Manhole 1.5x1.5 for Rainwater Drainage Network Zone 3	3	10-Jan-26	13-Jan-26	18-Nov-26	22-Nov-26	$5,317.56	$5,317.56	100%
MOD-RWN-	Install cover and frame Concrete Manhole 1.5x1.5 for Rainwater Drainage Network Zone	2	07-Jan-26	10-Jan-26	16-Nov-26	18-Nov-26	$7,090.09	$7,090.09	100%
MOD-RWN-	Masonry/benching works inside Concrete Manhole 1.5x1.5 for Rainwater Drainage Netw	5	01-Jan-26	07-Jan-26	10-Nov-26	16-Nov-26	$26,587.82	$26,587.82	100%
MOD-RWN-	Roof slab with openings Concrete Manhole 1.5x1.5 for Rainwater Drainage Network Zon	4	28-Dec-25	01-Jan-26	05-Nov-26	10-Nov-26	$88,626.07	$88,626.07	100%
MOD-RWN-	Wall reinforcement and casting Concrete Manhole 1.5x1.5 for Rainwater Drainage Netw	8	18-Dec-25	28-Dec-25	27-Oct-26	05-Nov-26	$106,351.29	$106,351.29	100%
MOD-RWN-	Base slab and wall shuttering Concrete Manhole 1.5x1.5 for Rainwater Drainage Networl	4	14-Dec-25	18-Dec-25	22-Oct-26	27-Oct-26	$108,123.81	$108,123.81	100%
MOD-RWN-	Excavation Concrete Manhole 1.5x1.5 for Rainwater Drainage Network Zone 3	6	07-Dec-25	14-Dec-25	15-Oct-26	22-Oct-26	$12,407.65	$12,407.65	100%
Concrete Manholes for 1000x1000 Box Pipes		36	07-Dec-25	18-Jan-26	15-Oct-26	26-Nov-26	$196,825.07	$196,825.07	100%
MOD-RWN-	Backfill in layers Concrete Manhole 1x1 for Rainwater Drainage Network Zone 3	5	12-Jan-26	18-Jan-26	21-Nov-26	26-Nov-26	$2,952.38	$2,952.38	100%
MOD-RWN-	Install cover and frame Concrete Manhole 1x1 for Rainwater Drainage Network Zone 3	4	07-Jan-26	12-Jan-26	16-Nov-26	21-Nov-26	$3,936.50	$3,936.50	100%
MOD-RWN-	Masonry/benching works inside Concrete Manhole 1x1 for Rainwater Drainage Network Z	7	30-Dec-25	07-Jan-26	08-Nov-26	16-Nov-26	$14,761.88	$14,761.88	100%
MOD-RWN-	Roof slab with openings Concrete Manhole 1x1 for Rainwater Drainage Network Zone 3	4	25-Dec-25	30-Dec-25	03-Nov-26	08-Nov-26	$49,206.27	$49,206.27	100%
MOD-RWN-	Wall reinforcement and casting Concrete Manhole 1x1 for Rainwater Drainage Network Z	6	18-Dec-25	25-Dec-25	27-Oct-26	03-Nov-26	$59,047.52	$59,047.52	100%
MOD-RWN-	Base slab and wall shuttering Concrete Manhole 1x1 for Rainwater Drainage Network Zo	4	14-Dec-25	18-Dec-25	22-Oct-26	27-Oct-26	$60,031.65	$60,031.65	100%
MOD-RWN-	Excavation Concrete Manhole 1x1 for Rainwater Drainage Network Zone 3	6	07-Dec-25	14-Dec-25	15-Oct-26	22-Oct-26	$6,888.88	$6,888.88	100%
Chambers and Catch Basins		5	11-Jan-26	17-Jan-26	15-Oct-26	21-Oct-26	$16,809.98	$16,809.98	100%
Precast Chambers for Absorption Pits		5	11-Jan-26	17-Jan-26	15-Oct-26	21-Oct-26	$16,809.98	$16,809.98	100%
MOD-RWN-	Backfill and compact Absorption Pit for Rainwater Drainage Network Zone 3	5	11-Jan-26	17-Jan-26	15-Oct-26	21-Oct-26	$16,809.98	$16,809.98	100%
Gully Outfalls to Swales		18	28-Dec-25	18-Jan-26	15-Oct-26	05-Nov-26	$49,531.52	$49,531.52	100%
Gully Outfalls to Swales		2	14-Jan-26	17-Jan-26	18-Oct-26	20-Oct-26	$14,151.86	$14,151.86	100%
MOD-RWN-	Compact and shape terrain Gully Outfall to Swales for Rainwater Drainage Network Zone	2	14-Jan-26	17-Jan-26	18-Oct-26	20-Oct-26	$14,151.86	$14,151.86	100%
Riprap Works & Protection		18	28-Dec-25	18-Jan-26	15-Oct-26	05-Nov-26	$35,379.65	$35,379.65	100%
MOD-RWN-	Ensure hydraulic flow direction for Rainwater Drainage Network Zone 3	2	15-Jan-26	18-Jan-26	03-Nov-26	05-Nov-26	$5,306.95	$5,306.95	100%
MOD-RWN-	Compact edges for Rainwater Drainage Network Zone 3	3	12-Jan-26	15-Jan-26	31-Oct-26	03-Nov-26	$7,075.93	$7,075.93	100%
MOD-RWN-	Place riprap/stone layer for Rainwater Drainage Network Zone 3	10	31-Dec-25	12-Jan-26	19-Oct-26	31-Oct-26	$19,458.81	$19,458.81	100%
MOD-RWN-	Lay filter fabric/membrane for Rainwater Drainage Network Zone 3	3	28-Dec-25	31-Dec-25	15-Oct-26	19-Oct-26	$3,537.97	$3,537.97	100%
Backfilling & Bedding		12	04-Jan-26	18-Jan-26	12-Oct-26	26-Oct-26	$76,481.68	$76,481.68	100%
Gravel Bedding & Filter Cloth for uPVC Drain Pipes		12	04-Jan-26	18-Jan-26	12-Oct-26	26-Oct-26	$76,481.68	$76,481.68	100%
MOD-RWN-	Final fill and trench restoration for Rainwater Drainage Network Zone 3	12	04-Jan-26	18-Jan-26	12-Oct-26	26-Oct-26	$76,481.68	$76,481.68	100%
Deep Basin for Groundwater Collection (2.5–3.0m)		7	10-Jan-26	18-Jan-26	18-Oct-26	26-Oct-26	$128,325.52	$128,325.52	100%
MOD-RWN-DB	Backfill in controlled layers for Rainwater Drainage Network Zone 3	7	10-Jan-26	18-Jan-26	18-Oct-26	26-Oct-26	$128,325.52	$128,325.52	100%
Potable Water Network Zone 3		67	19-Oct-25	18-Jan-26	03-Oct-26	19-Dec-26	5,150,041.3	$5,150,041.33	100%
Valve Installation & Chambers		20	27-Dec-25	18-Jan-26	04-Oct-26	27-Oct-26	$47,445.51	$47,445.51	100%
MOD-PWN-VC	Tagging & Painting for Potable Water Network Zone 3	6	12-Jan-26	18-Jan-26	20-Oct-26	27-Oct-26	$15,815.17	$15,815.17	100%
MOD-PWN-VC	Fixing Covers, Gratings, Frames for Potable Water Network Zone 3	14	27-Dec-25	11-Jan-26	04-Oct-26	20-Oct-26	$31,630.34	$31,630.34	100%
Flow Meter Installation		21	18-Dec-25	11-Jan-26	29-Oct-26	23-Nov-26	$33,844.89	$33,844.89	100%

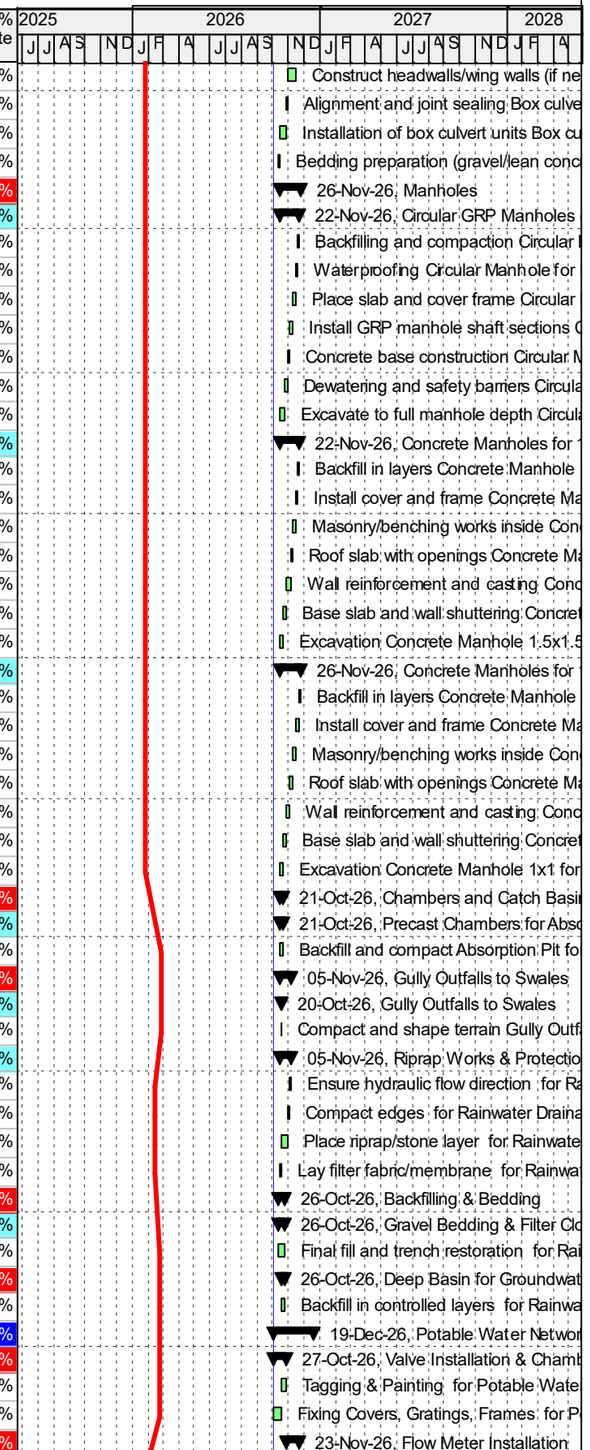


Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary

TASK filter: Activity % (Faiiled Start).

© Oracle Corporation

Development of Phase One – Part Two – Third Industrial


Activity ID	Activity Name	Original Duration	BL Project Start	BL Project Finish	Start	Finish	Budgeted Total Cost	Remaining Total Cost	Schedule % Complete
MOD-PWN-FM	Calibration & Commissioning for Potable Water Network Zone 3	3	08-Jan-26	11-Jan-26	19-Nov-26	23-Nov-26	$3,076.81	$3,076.81	100%
MOD-PWN-FM	Wiring/Cabling if applicable for Potable Water Network Zone 3	8	30-Dec-25	07-Jan-26	10-Nov-26	19-Nov-26	$9,230.42	$9,230.42	100%
MOD-PWN-FM	Flowmeter Installation & Pipe Integration for Potable Water Network Zone 3	10	18-Dec-25	29-Dec-25	29-Oct-26	10-Nov-26	$21,537.66	$21,537.66	100%
Washout & Air Valve Chambers		2	01-Jan-26	03-Jan-26	10-Oct-26	12-Oct-26	$19,468.09	$19,468.09	100%
MOD-PWN-W/	Backfilling & Final Finishing for Potable Water Network Zone 3	2	01-Jan-26	03-Jan-26	10-Oct-26	12-Oct-26	$19,468.09	$19,468.09	100%
Pumping Station (Structure & Civil Works)		66	19-Oct-25	04-Jan-26	03-Oct-26	17-Dec-26	$473,145.06	$473,145.06	100%
MOD-PWN-PS	Internal piping & embedded sleeves for Potable Water Network Zone 3	13	15-Nov-25	30-Nov-25	29-Oct-26	12-Nov-26	$78,857.51	$78,857.51	100%
MOD-PWN-PS	Access Ladders, Tight Cover, Surface Guttering for Potable Water Network Zone 3	5	09-Nov-25	15-Nov-25	24-Oct-26	28-Oct-26	$78,857.51	$78,857.51	100%
MOD-PWN-PS	Reinforced Concrete/GRP Shell Construction for Potable Water Network Zone 3	8	30-Oct-25	09-Nov-25	14-Oct-26	22-Oct-26	$78,857.51	$78,857.51	100%
MOD-PWN-PS	Excavation & Blinding for Potable Water Network Zone 3	10	19-Oct-25	30-Oct-25	03-Oct-26	13-Oct-26	$78,857.51	$78,857.51	100%
MOD-PWN-PS	Backfilling & External Finishes for Potable Water Network Zone 3	17	15-Dec-25	04-Jan-26	29-Nov-26	17-Dec-26	$78,857.51	$78,857.51	100%
MOD-PWN-PS	Pump Base Pads + Grouting for Potable Water Network Zone 3	13	30-Nov-25	15-Dec-25	14-Nov-26	28-Nov-26	$78,857.51	$78,857.51	100%
Pump Station Building		31	30-Nov-25	05-Jan-26	14-Nov-26	19-Dec-26	$183,637.93	$183,637.93	100%
MOD-PWN-PB	Finishes, Doors, Ventilation for Potable Water Network Zone 3	13	21-Dec-25	05-Jan-26	05-Dec-26	19-Dec-26	$78,857.51	$78,857.51	100%
MOD-PWN-PB	5-ton Hoist Installation for Potable Water Network Zone 3	5	15-Dec-25	21-Dec-25	29-Nov-26	03-Dec-26	$25,922.91	$25,922.91	100%
MOD-PWN-PB	Structure Construction (as per architectural drawings) for Potable Water Network Zone 3	13	30-Nov-25	15-Dec-25	14-Nov-26	28-Nov-26	$78,857.51	$78,857.51	100%
Pumping Equipment & Fire Systems		28	17-Dec-25	18-Jan-26	14-Nov-26	15-Dec-26	$946,290.12	$946,290.12	100%
MOD-PWN-PE	Electric Fire Water Pump (64 L/s @ 60 m) for Potable Water Network Zone 3	8	03-Jan-26	11-Jan-26	30-Nov-26	08-Dec-26	$96,010.78	$96,010.78	100%
MOD-PWN-PE	Main Pumps (250 kW, 295 L/s @ 60 m head) for Potable Water Network Zone 3	14	17-Dec-25	01-Jan-26	14-Nov-26	29-Nov-26	$438,877.07	$438,877.07	100%
MOD-PWN-PE	Flow meter on 800mm pipe including flow meter chamber and 2-2.5m depth for Potable	3	15-Jan-26	18-Jan-26	13-Dec-26	15-Dec-26	$82,788.23	$82,788.23	100%
MOD-PWN-PE	MCC & DB panel installation for Potable Water Network Zone 3	2	13-Jan-26	14-Jan-26	10-Dec-26	12-Dec-26	$78,857.51	$78,857.51	100%
MOD-PWN-PE	Pipework connections within Pump Room for Potable Water Network Zone 3	5	07-Jan-26	12-Jan-26	05-Dec-26	09-Dec-26	$78,857.51	$78,857.51	100%
MOD-PWN-PE	Submersible Fire Pumps (2 pcs, 10 L/s @ 10 m) for Potable Water Network Zone 3	4	03-Jan-26	06-Jan-26	30-Nov-26	03-Dec-26	$36,483.86	$36,483.86	100%
MOD-PWN-PE	Electric Jockey Pump for Potable Water Network Zone 3	6	03-Jan-26	08-Jan-26	30-Nov-26	06-Dec-26	$48,005.39	$48,005.39	100%
MOD-PWN-PE	Diesel Fire Water Pump (64 L/s @ 60 m) for Potable Water Network Zone 3	6	03-Jan-26	08-Jan-26	30-Nov-26	06-Dec-26	$86,409.76	$86,409.76	100%
Surge Protection		5	13-Jan-26	18-Jan-26	10-Dec-26	15-Dec-26	$28,227.66	$28,227.66	100%
MOD-PWN-SP	Pipe Integration as per Surge Analysis for Potable Water Network Zone 3	1	18-Jan-26	18-Jan-26	15-Dec-26	15-Dec-26	$5,645.53	$5,645.53	100%
MOD-PWN-SP	Surge Vessel Installation for Potable Water Network Zone 3	4	13-Jan-26	17-Jan-26	10-Dec-26	14-Dec-26	$22,582.13	$22,582.13	100%
Power & Generator System		12	03-Jan-26	15-Jan-26	30-Nov-26	13-Dec-26	2,851,518.7	$2,851,518.70	100%
MOD-PWN-PG	Earthing & Commissioning for Potable Water Network Zone 3	2	14-Jan-26	15-Jan-26	12-Dec-26	13-Dec-26	$142,575.94	$142,575.94	100%
MOD-PWN-PG	Electrical Cabling, Circuit Breakers for Potable Water Network Zone 3	4	10-Jan-26	13-Jan-26	07-Dec-26	10-Dec-26	$142,575.94	$142,575.94	100%
MOD-PWN-PG	Canopy, Foundation & Fuel Tank for Potable Water Network Zone 3	6	03-Jan-26	08-Jan-26	30-Nov-26	06-Dec-26	$285,151.87	$285,151.87	100%
MOD-PWN-PG	500 kVA Standby Generator Installation for Potable Water Network Zone 3	4	03-Jan-26	06-Jan-26	30-Nov-26	03-Dec-26	2,281,214.9	$2,281,214.96	100%
Chlorination System		14	03-Jan-26	18-Jan-26	30-Nov-26	15-Dec-26	$518,457.97	$518,457.97	100%
MOD-PWN-CS	Control Integration for Potable Water Network Zone 3	3	15-Jan-26	18-Jan-26	13-Dec-26	15-Dec-26	$51,845.80	$51,845.80	100%
MOD-PWN-CS	Connections to Main Line or Disinfection Chamber for Potable Water Network Zone 3	4	11-Jan-26	14-Jan-26	08-Dec-26	12-Dec-26	$103,691.59	$103,691.59	100%
MOD-PWN-CS	Chlorination Device Supply & Installation for Potable Water Network Zone 3	7	03-Jan-26	10-Jan-26	30-Nov-26	07-Dec-26	$362,920.58	$362,920.58	100%
Street Lighting		6	12-Jan-26	18-Jan-26	30-Nov-26	07-Dec-26	$48,005.39	$48,005.39	100%
MOD-PWN-SL·	Testing & Lighting Commissioning for Potable Water Network Zone 3	6	12-Jan-26	18-Jan-26	30-Nov-26	07-Dec-26	$24,002.70	$24,002.70	100%
MOD-PWN-SL·	Connection to Main Supply for Potable Water Network Zone 3	6	12-Jan-26	18-Jan-26	30-Nov-26	07-Dec-26	$24,002.70	$24,002.70	100%
Irrigation Network Zone 3		10	31-Dec-25	11-Jan-26	03-Nov-26	15-Nov-26	$8,967.46	$8,967.46	100%
Flow Meter Chambers		10	31-Dec-25	11-Jan-26	03-Nov-26	15-Nov-26	$8,967.46	$8,967.46	100%
MOD-IRN-FC-1	Cover and Access Arrangement Flow Meter Chamber for Irrigation Network Zone 3	4	07-Jan-26	11-Jan-26	10-Nov-26	15-Nov-26	$2,241.87	$2,241.87	100%
MOD-IRN-FC-1	Testing & Calibration Flow Meter Chamber for Irrigation Network Zone 3	6	31-Dec-25	06-Jan-26	03-Nov-26	10-Nov-26	$6,725.60	$6,725.60	100%
Rainwater Collection Ponds Zone 3		46	10-Mar-26	17-Aug-26	06-Jan-27	20-Mar-27	$836,263.27	$836,263.27	100%
Excavation for Rainwater Drainage Pond		2	10-Mar-26	14-Mar-26	06-Jan-27	09-Jan-27	$5,919.63	$5,919.63	100%
Deep excavation, backfill, disposal for pond formation		2	10-Mar-26	14-Mar-26	06-Jan-27	09-Jan-27	$5,919.63	$5,919.63	100%
MOD-RCP-E	Final trimming and profiling for Rainwater Collection Ponds Zone 3	2	10-Mar-26	14-Mar-26	06-Jan-27	09-Jan-27	$5,919.63	$5,919.63	100%
Backfilling Works		5	23-Jul-26	29-Jul-26	16-Jan-27	21-Jan-27	$42,226.67	$42,226.67	100%
MOD-RCP-BW	Final leveling and approval for Rainwater Collection Ponds Zone 3	5	23-Jul-26	29-Jul-26	16-Jan-27	21-Jan-27	$42,226.67	$42,226.67	100%

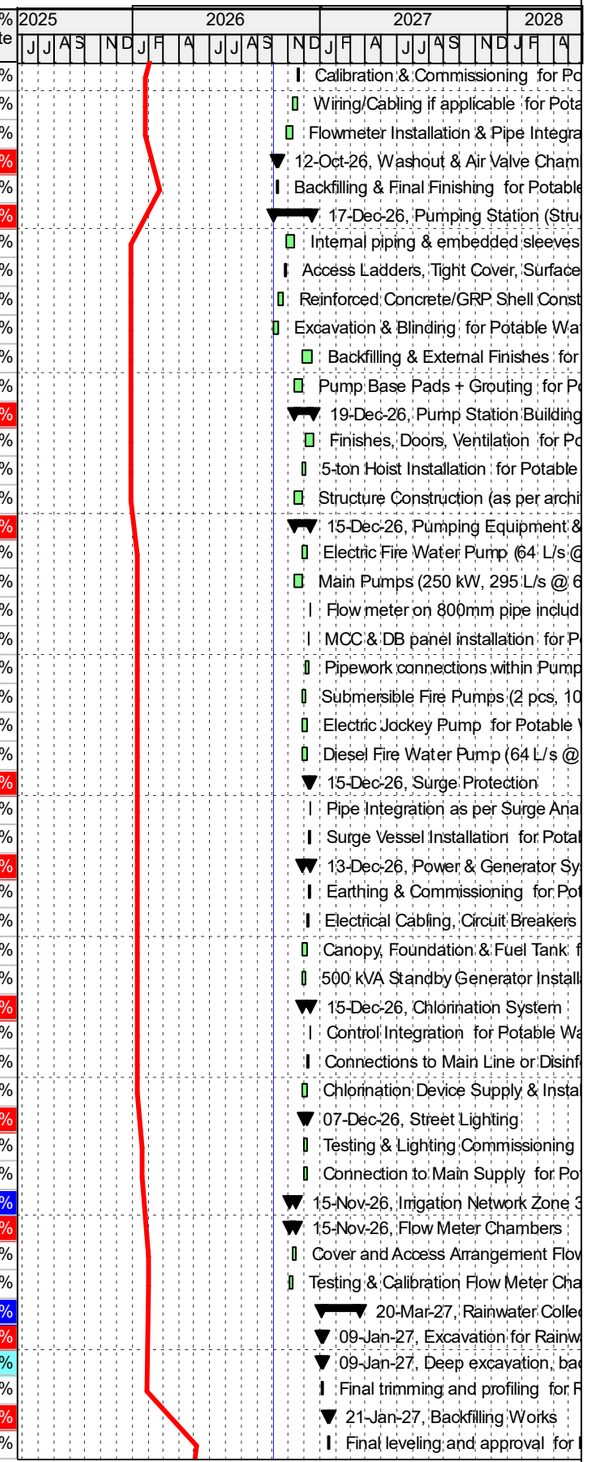

© Oracle Corporation

Development of Phase One – Part Two – Third Industrial

Activity ID	Activity Name	Original Duration	BL Project Start	BL Project Finish	Start	Finish	Budgeted Total Cost	Remaining Total Cost	Schedule % Complete
Geotextile & Bedding		38	04-Jul-26	17-Aug-26	17-Jan-27	20-Mar-27	$788,116.97	$788,116.97	100%
Installation of geotextile lining and coarse sand bedding		38	04-Jul-26	17-Aug-26	17-Jan-27	20-Mar-27	$788,116.97	$788,116.97	100%
MOD-RCP-(	Compact and level bedding for Rainwater Collection Ponds Zone 3	17	28-Jul-26	17-Aug-26	13-Feb-27	20-Mar-27	$358,234.99	$358,234.99	100%
MOD-RCP-(	Place 500mm thick coarse sand bedding for Rainwater Collection Ponds Zone 3	21	04-Jul-26	28-Jul-26	17-Jan-27	11-Feb-27	$429,881.98	$429,881.98	100%
Road Crossing Zone 3		118	07-May-26	07-Oct-26	16-Jan-27	24-Jun-27	$341,187.70	$341,187.70	98.01%
uPVC Road Crossing Pipes		27	07-May-26	22-Jun-26	16-Jan-27	24-Feb-27	$120,284.48	$120,284.48	100%
Installation of uPVC pipes of various diameters crossing roadways		27	07-May-26	22-Jun-26	16-Jan-27	24-Feb-27	$120,284.48	$120,284.48	100%
MOD-ROC-F	Reinstatement of road surface for Road Crossing Zone 3	6	15-Jun-26	22-Jun-26	11-Feb-27	24-Feb-27	$15,035.56	$15,035.56	100%
MOD-ROC-F	Backfilling and compaction in layers for Road Crossing Zone 3	10	26-May-26	15-Jun-26	28-Jan-27	11-Feb-27	$30,071.12	$30,071.12	100%
MOD-ROC-F	Testing of installed pipeline for Road Crossing Zone 3	6	19-May-26	26-May-26	21-Jan-27	28-Jan-27	$15,035.56	$15,035.56	100%
MOD-ROC-F	Placement of supports and protection around the pipe for Road Crossing Zone 3	5	07-May-26	19-May-26	16-Jan-27	21-Jan-27	$60,142.24	$60,142.24	100%
GRP Road Crossing Pipes		91	22-Jun-26	07-Oct-26	24-Feb-27	24-Jun-27	$220,903.22	$220,903.22	96.92%
Installation of GRP pipes (800mm–1000mm dia) for road crossings		91	22-Jun-26	07-Oct-26	24-Feb-27	24-Jun-27	$220,903.22	$220,903.22	96.92%
MOD-ROC-(	Reinstate road surface (asphalt/concrete) for Road Crossing Zone 3	8	28-Sep-26	07-Oct-26	16-Jun-27	24-Jun-27	$11,328.37	$11,328.37	40%
MOD-ROC-(	Backfill and compact in layers for Road Crossing Zone 3	15	09-Sep-26	28-Sep-26	30-May-27	15-Jun-27	$22,656.74	$22,656.74	100%
MOD-ROC-(	Perform leak testing as per specifications for Road Crossing Zone 3	5	03-Sep-26	09-Sep-26	24-May-27	29-May-27	$5,664.19	$5,664.19	100%
MOD-ROC-(	Provide structural supports and closure at both ends for Road Crossing Zone 3	9	24-Aug-26	03-Sep-26	09-May-27	23-May-27	$22,656.74	$22,656.74	100%
MOD-ROC-(	Install GRP pipe (800mm & 1000mm dia) for Road Crossing Zone 3	21	30-Jul-26	24-Aug-26	14-Apr-27	08-May-27	$90,626.96	$90,626.96	100%
MOD-ROC-(	Lay compacted granular bedding for Road Crossing Zone 3	16	12-Jul-26	30-Jul-26	27-Mar-27	13-Apr-27	$33,985.11	$33,985.11	100%
MOD-ROC-(	Excavate trench across road at designed depth for Road Crossing Zone 3	12	28-Jun-26	12-Jul-26	06-Mar-27	25-Mar-27	$22,656.74	$22,656.74	100%
MOD-ROC-(	Set out location and coordinate with road authority for Road Crossing Zone 3	5	22-Jun-26	28-Jun-26	24-Feb-27	06-Mar-27	$11,328.37	$11,328.37	100%
Zone 2		370	06-Dec-25	07-Oct-26	22-Jul-26 A	27-Jul-27	4,256,150.0	$4,256,150.01	99.68%
Sewerage Network Zone 2		60	06-Dec-25	04-Mar-26	09-Oct-26	08-Dec-26	$626,218.36	$626,218.36	100%
Pipework: Supply, Installation, and Testing		15	20-Jan-26	03-Feb-26	11-Nov-26	25-Nov-26	$20,836.71	$20,836.71	100%
HDPE Pressure Pipes Installation (250mm–630mm)		15	20-Jan-26	03-Feb-26	11-Nov-26	25-Nov-26	$20,836.71	$20,836.71	100%
MOD-SWN-	Backfilling & Warrning Tape HDPE for Sewerage Network Zone 2	15	20-Jan-26	03-Feb-26	11-Nov-26	25-Nov-26	$20,836.71	$20,836.71	100%
Fittings and Valves		27	21-Dec-25	20-Jan-26	26-Oct-26	26-Nov-26	$61,422.41	$61,422.41	100%
MOD-SWN-FV-	Supply & Installation of HDPE Elbows for Sewerage Network Zone 2	6	21-Dec-25	27-Dec-25	26-Oct-26	02-Nov-26	$13,652.43	$13,652.43	100%
MOD-SWN-FV-	Jointing & Piping Accessories Installation for Sewerage Network Zone 2	3	18-Jan-26	20-Jan-26	23-Nov-26	26-Nov-26	$6,142.24	$6,142.24	100%
MOD-SWN-FV-	Air Breather & Air Release Valves Installation for Sewerage Network Zone 2	10	06-Jan-26	17-Jan-26	11-Nov-26	23-Nov-26	$23,181.49	$23,181.49	100%
MOD-SWN-FV-	Drain Valves Installation for Sewerage Network Zone 2	4	01-Jan-26	05-Jan-26	07-Nov-26	11-Nov-26	$8,785.65	$8,785.65	100%
MOD-SWN-FV-	Gate Valves Installation for Sewerage Network Zone 2	4	28-Dec-25	31-Dec-25	02-Nov-26	07-Nov-26	$9,660.60	$9,660.60	100%
Valve & Flow Meter Chambers		51	06-Dec-25	10-Feb-26	18-Oct-26	08-Dec-26	$34,447.83	$34,447.83	100%
Valve Chambers Construction		30	06-Dec-25	04-Jan-26	18-Oct-26	17-Nov-26	$4,136.44	$4,136.44	100%
MOD-SWN-	Test Valve Chamber for Sewerage Network Zone 2	15	06-Dec-25	20-Dec-25	18-Oct-26	02-Nov-26	$1,378.81	$1,378.81	100%
MOD-SWN-	Backfilling Valve Chamber for Sewerage Network Zone 2	15	21-Dec-25	04-Jan-26	02-Nov-26	17-Nov-26	$2,757.62	$2,757.62	100%
Water Drain Chambers Construction		30	25-Dec-25	23-Jan-26	28-Oct-26	27-Nov-26	$13,436.57	$13,436.57	100%
MOD-SWN-	Test Water Drain Chamber for Sewerage Network Zone 2	15	25-Dec-25	08-Jan-26	28-Oct-26	12-Nov-26	$4,478.86	$4,478.86	100%
MOD-SWN-	Backfilling Water Drain Chamber for Sewerage Network Zone 2	15	09-Jan-26	23-Jan-26	12-Nov-26	27-Nov-26	$8,957.71	$8,957.71	100%
Discharge Chambers Construction		30	07-Jan-26	05-Feb-26	03-Nov-26	03-Dec-26	$9,386.17	$9,386.17	100%
MOD-SWN-	Test Discharge Chamber for Sewerage Network Zone 2	15	07-Jan-26	21-Jan-26	03-Nov-26	18-Nov-26	$3,128.72	$3,128.72	100%
MOD-SWN-	Backfilling Discharge Chamber for Sewerage Network Zone 2	15	22-Jan-26	05-Feb-26	18-Nov-26	03-Dec-26	$6,257.45	$6,257.45	100%
Flow Meter Chambers Construction		35	07-Jan-26	10-Feb-26	03-Nov-26	08-Dec-26	$7,488.66	$7,488.66	100%
MOD-SWN-	Flow Meter Chambers Construction Flow Meter Chamber for Sewerage Network Zone 2	5	07-Jan-26	11-Jan-26	03-Nov-26	08-Nov-26	$4,493.20	$4,493.20	100%
MOD-SWN-	Test Flow Meter Chamber for Sewerage Network Zone 2	15	12-Jan-26	26-Jan-26	08-Nov-26	23-Nov-26	$998.49	$998.49	100%
MOD-SWN-	Backfilling Flow Meter Chamber for Sewerage Network Zone 2	15	27-Jan-26	10-Feb-26	23-Nov-26	08-Dec-26	$1,996.98	$1,996.98	100%
Manholes		36	21-Dec-25	04-Mar-26	09-Oct-26	14-Nov-26	$509,511.41	$509,511.41	100%
1200mm GRP Manholes with Backdrop		30	21-Dec-25	19-Jan-26	09-Oct-26	08-Nov-26	$253,577.48	$253,577.48	100%
MOD-SWN-	Test 1.2m GRP for Sewerage Network Zone 2	15	21-Dec-25	04-Jan-26	09-Oct-26	24-Oct-26	$84,525.83	$84,525.83	100%
MOD-SWN-	Backfilling 1.2m GRP for Sewerage Network Zone 2	15	05-Jan-26	19-Jan-26	24-Oct-26	08-Nov-26	$169,051.65	$169,051.65	100%

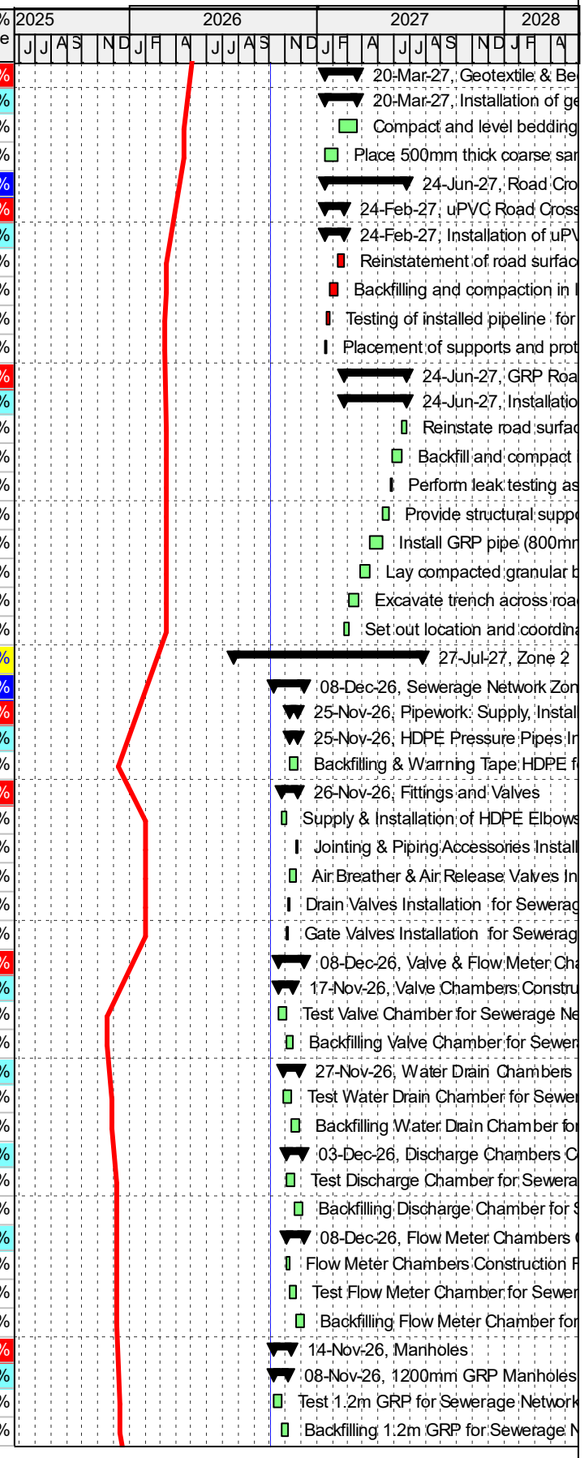


Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary

TASK filter: Activity % (Faiiled Start).

© Oracle Corporation

Development of Phase One – Part Two – Third Industrial

Activity ID	Activity Name	Original Duration	BL Project Start	BL Project Finish	Start	Finish	Budgeted Total Cost	Remaining Total Cost	Schedule % Complete
1500mm GRP Manholes (Standard & Backdrop)		30	11-Jan-26	09-Feb-26	12-Oct-26	11-Nov-26	$240,158.92	$240,158.92	100%
MOD-SWN-	Test 1.5m GRP for Sewerage Network Zone 2	15	11-Jan-26	25-Jan-26	12-Oct-26	27-Oct-26	$80,052.97	$80,052.97	100%
MOD-SWN-	Backfilling 1.5m GRP for Sewerage Network Zone 2	15	26-Jan-26	09-Feb-26	27-Oct-26	11-Nov-26	$160,105.94	$160,105.94	100%
1800mm GRP Manholes (Standard & Backdrop)		30	28-Jan-26	26-Feb-26	14-Oct-26	13-Nov-26	$11,980.90	$11,980.90	100%
MOD-SWN-	Test 1.8m GRP for Sewerage Network Zone 2	15	28-Jan-26	11-Feb-26	14-Oct-26	29-Oct-26	$3,993.63	$3,993.63	100%
MOD-SWN-	Backfilling 1.8m GRP for Sewerage Network Zone 2	15	12-Feb-26	26-Feb-26	29-Oct-26	13-Nov-26	$7,987.27	$7,987.27	100%
2000mm GRP Manholes (Standard & Backdrop)		30	03-Feb-26	04-Mar-26	15-Oct-26	14-Nov-26	$3,794.11	$3,794.11	100%
MOD-SWN-	Test 2m GRP for Sewerage Network Zone 2	15	03-Feb-26	17-Feb-26	15-Oct-26	30-Oct-26	$1,264.70	$1,264.70	100%
MOD-SWN-	Backfilling 2m GRP for Sewerage Network Zone 2	15	18-Feb-26	04-Mar-26	30-Oct-26	14-Nov-26	$2,529.41	$2,529.41	100%
Rainwater Drainage Network Zone 2		31	13-Dec-25	18-Jan-26	05-Oct-26	10-Nov-26	1,491,938.6	$1,491,938.63	100%
Precast Concrete Box Culverts		31	13-Dec-25	18-Jan-26	05-Oct-26	09-Nov-26	$964,996.20	$964,996.20	100%
Box Culverts (500x500mm to 3500x800mm)		26	13-Dec-25	18-Jan-26	10-Oct-26	09-Nov-26	$954,031.60	$954,031.60	100%
MOD-RWN-	Backfilling and compaction Box culvert for Rainwater Drainage Network Zone 2	6	07-Jan-26	14-Jan-26	28-Oct-26	04-Nov-26	$74,202.46	$74,202.46	100%
MOD-RWN-	Construct headwalls/wing walls (if needed) Box culvert for Rainwater Drainage Network Zo	7	30-Dec-25	07-Jan-26	20-Oct-26	28-Oct-26	$106,003.51	$106,003.51	100%
MOD-RWN-	Alignment and joint sealing Box culvert for Rainwater Drainage Network Zone 2	4	25-Dec-25	30-Dec-25	15-Oct-26	20-Oct-26	$74,202.46	$74,202.46	100%
MOD-RWN-	Installation of box culvert units Box culvert for Rainwater Drainage Network Zone 2	5	13-Dec-25	25-Dec-25	10-Oct-26	15-Oct-26	$636,021.07	$636,021.07	100%
MOD-RWN-	Surface finishing Box culvert for Rainwater Drainage Network Zone 2	3	15-Jan-26	18-Jan-26	05-Nov-26	09-Nov-26	$63,602.11	$63,602.11	100%
Box Culverts at Road Intersections		26	20-Dec-25	18-Jan-26	05-Oct-26	03-Nov-26	$10,964.60	$10,964.60	100%
MOD-RWN-	Backfilling and surface reinstatement for Rainwater Drainage Network Zone 2	8	10-Jan-26	18-Jan-26	25-Oct-26	03-Nov-26	$216.41	$216.41	100%
MOD-RWN-	Joint treatment and testing for Rainwater Drainage Network Zone 2	12	25-Dec-25	08-Jan-26	11-Oct-26	24-Oct-26	$288.54	$288.54	100%
MOD-RWN-	Construct connection chambers (if needed) for Rainwater Drainage Network Zone 2	1	24-Dec-25	25-Dec-25	10-Oct-26	10-Oct-26	$1,082.03	$1,082.03	100%
MOD-RWN-	Install precast box culvert for Rainwater Drainage Network Zone 2	4	20-Dec-25	24-Dec-25	05-Oct-26	08-Oct-26	$9,377.62	$9,377.62	100%
Manholes		25	17-Dec-25	18-Jan-26	12-Oct-26	10-Nov-26	$473,872.95	$473,872.95	100%
Circular GRP Manholes (1200–1800mm dia)		5	13-Jan-26	18-Jan-26	17-Oct-26	22-Oct-26	$16,009.61	$16,009.61	100%
MOD-RWN-	Backfilling and compaction Circular Manhole for Rainwater Drainage Network Zone 2	2	17-Jan-26	18-Jan-26	20-Oct-26	22-Oct-26	$6,861.26	$6,861.26	100%
MOD-RWN-	Waterproofing Circular Manhole for Rainwater Drainage Network Zone 2	2	13-Jan-26	15-Jan-26	17-Oct-26	19-Oct-26	$9,148.35	$9,148.35	100%
Concrete Manholes for 1500x1500 Box Pipes		7	03-Jan-26	11-Jan-26	17-Oct-26	25-Oct-26	$77,990.94	$77,990.94	100%
MOD-RWN-	Backfill in layers Concrete Manhole 1.5x1.5 for Rainwater Drainage Network Zone 2	3	07-Jan-26	11-Jan-26	21-Oct-26	25-Oct-26	$10,635.13	$10,635.13	100%
MOD-RWN-	Install cover and frame Concrete Manhole 1.5x1.5 for Rainwater Drainage Network Zone	2	05-Jan-26	07-Jan-26	19-Oct-26	21-Oct-26	$14,180.17	$14,180.17	100%
MOD-RWN-	Masonry/benching works inside Concrete Manhole 1.5x1.5 for Rainwater Drainage Netw	2	03-Jan-26	05-Jan-26	17-Oct-26	19-Oct-26	$53,175.64	$53,175.64	100%
Concrete Manholes for 1000x1000 Box Pipes		25	17-Dec-25	15-Jan-26	12-Oct-26	10-Nov-26	$379,872.39	$379,872.39	100%
MOD-RWN-	Backfill in layers Concrete Manhole 1x1 for Rainwater Drainage Network Zone 2	3	12-Jan-26	15-Jan-26	07-Nov-26	10-Nov-26	$5,904.75	$5,904.75	100%
MOD-RWN-	Install cover and frame Concrete Manhole 1x1 for Rainwater Drainage Network Zone 2	4	07-Jan-26	12-Jan-26	02-Nov-26	07-Nov-26	$7,873.00	$7,873.00	100%
MOD-RWN-	Masonry/benching works inside Concrete Manhole 1x1 for Rainwater Drainage Network Z	5	01-Jan-26	07-Jan-26	27-Oct-26	02-Nov-26	$29,523.76	$29,523.76	100%
MOD-RWN-	Roof slab with openings Concrete Manhole 1x1 for Rainwater Drainage Network Zone 2	6	25-Dec-25	01-Jan-26	20-Oct-26	27-Oct-26	$98,412.54	$98,412.54	100%
MOD-RWN-	Wall reinforcement and casting Concrete Manhole 1x1 for Rainwater Drainage Network Z	5	20-Dec-25	25-Dec-25	14-Oct-26	20-Oct-26	$118,095.04	$118,095.04	100%
MOD-RWN-	Base slab and wall shuttering Concrete Manhole 1x1 for Rainwater Drainage Network Zo	2	17-Dec-25	20-Dec-25	12-Oct-26	14-Oct-26	$120,063.30	$120,063.30	100%
Gully Outfalls to Swales		11	05-Jan-26	18-Jan-26	12-Oct-26	25-Oct-26	$53,069.48	$53,069.48	100%
Gully Outfalls to Swales		2	17-Jan-26	18-Jan-26	12-Oct-26	14-Oct-26	$28,303.72	$28,303.72	100%
MOD-RWN-	Compact and shape terrain Gully Outfall to Swales for Rainwater Drainage Network Zone	2	17-Jan-26	18-Jan-26	12-Oct-26	14-Oct-26	$28,303.72	$28,303.72	100%
Riprap Works & Protection		8	05-Jan-26	14-Jan-26	15-Oct-26	25-Oct-26	$24,765.76	$24,765.76	100%
MOD-RWN-	Ensure hydraulic flow direction for Rainwater Drainage Network Zone 2	3	11-Jan-26	14-Jan-26	21-Oct-26	25-Oct-26	$10,613.90	$10,613.90	100%
MOD-RWN-	Compact edges for Rainwater Drainage Network Zone 2	5	05-Jan-26	11-Jan-26	15-Oct-26	21-Oct-26	$14,151.86	$14,151.86	100%
Potable Water Network Zone 2		44	18-Dec-25	13-Jan-26	05-Oct-26	25-Nov-26	$201,516.98	$201,516.98	100%
Valve Installation & Chambers		10	21-Dec-25	31-Dec-25	05-Oct-26	17-Oct-26	$94,891.03	$94,891.03	100%
MOD-PWN-VC	Tagging & Painting for Potable Water Network Zone 2	4	28-Dec-25	31-Dec-25	12-Oct-26	17-Oct-26	$31,630.34	$31,630.34	100%
MOD-PWN-VC	Fixing Covers, Gratings, Frames for Potable Water Network Zone 2	6	21-Dec-25	27-Dec-25	05-Oct-26	12-Oct-26	$63,260.68	$63,260.68	100%
Flow Meter Installation		23	18-Dec-25	13-Jan-26	29-Oct-26	25-Nov-26	$67,689.77	$67,689.77	100%
MOD-PWN-FM	Calibration & Commissioning for Potable Water Network Zone 2	3	11-Jan-26	13-Jan-26	22-Nov-26	25-Nov-26	$6,153.62	$6,153.62	100%
MOD-PWN-FM	Wiring/Cabling if applicable for Potable Water Network Zone 2	8	01-Jan-26	10-Jan-26	12-Nov-26	22-Nov-26	$18,460.85	$18,460.85	100%

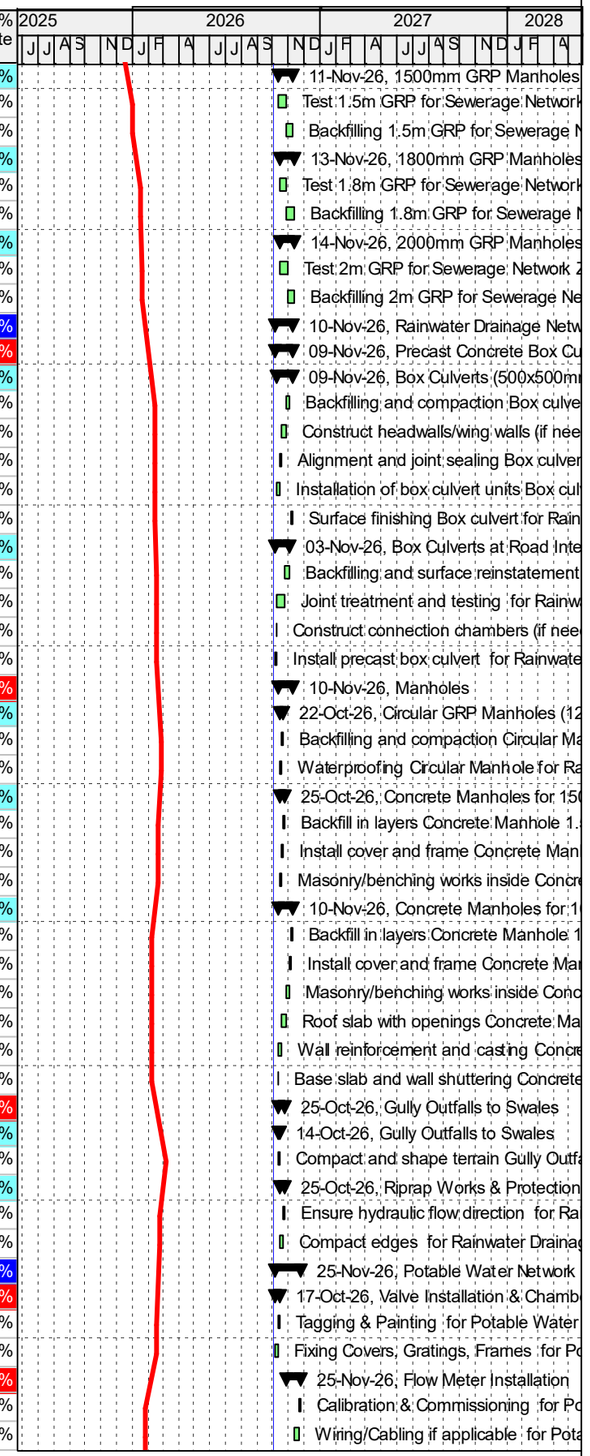


Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary

TASK filter: Activity % (Failed Start).

© Oracle Corporation

Development of Phase One – Part Two – Third Industrial

Activity ID	Activity Name	Original Duration	BL Project Start	BL Project Finish	Start	Finish	Budgeted Total Cost	Remaining Total Cost	Schedule % Complete
MOD-PWN-FM	Flowmeter Installation & Pipe Integration for Potable Water Network Zone 2	12	18-Dec-25	31-Dec-25	29-Oct-26	12-Nov-26	$43,075.31	$43,075.31	100%
Washout & Air Valve Chambers		2	06-Jan-26	07-Jan-26	10-Oct-26	12-Oct-26	$38,936.18	$38,936.18	100%
MOD-PWN-W/	Backfilling & Final Finishing for Potable Water Network Zone 2	2	06-Jan-26	07-Jan-26	10-Oct-26	12-Oct-26	$38,936.18	$38,936.18	100%
Irrigation Network Zone 2		7	11-Jan-26	18-Jan-26	31-Oct-26	08-Nov-26	$17,934.92	$17,934.92	100%
Flow Meter Chambers		7	11-Jan-26	18-Jan-26	31-Oct-26	08-Nov-26	$17,934.92	$17,934.92	100%
MOD-IRN-FC-5	Cover and Access Arrangement Flow Meter Chamber for Irrigation Network Zone 2	3	15-Jan-26	18-Jan-26	04-Nov-26	08-Nov-26	$4,483.73	$4,483.73	100%
MOD-IRN-FC-4	Testing & Calibration Flow Meter Chamber for Irrigation Network Zone 2	4	11-Jan-26	14-Jan-26	31-Oct-26	04-Nov-26	$13,451.19	$13,451.19	100%
Rainwater Collection Ponds Zone 2		192	07-Mar-26	27-Sep-26	22-Jul-26 A	01-Apr-27	$273,889.92	$273,889.92	100%
Excavation for Rainwater Drainage Pond		4	07-Mar-26	14-Mar-26	04-Jan-27	09-Jan-27	$3,946.42	$3,946.42	100%
Deep excavation, backfill, disposal for pond formation		4	07-Mar-26	14-Mar-26	04-Jan-27	09-Jan-27	$3,946.42	$3,946.42	100%
MOD-RCP-E	Final trimming and profiling for Rainwater Collection Ponds Zone 2	2	10-Mar-26	14-Mar-26	06-Jan-27	09-Jan-27	$1,691.32	$1,691.32	100%
MOD-RCP-E	Backfill selected areas as per design for Rainwater Collection Ponds Zone 2	2	07-Mar-26	10-Mar-26	04-Jan-27	06-Jan-27	$2,255.10	$2,255.10	100%
Backfilling Works		5	17-Aug-26	23-Aug-26	16-Jan-27	21-Jan-27	$12,064.76	$12,064.76	100%
MOD-RCP-BW	Final leveling and approval for Rainwater Collection Ponds Zone 2	5	17-Aug-26	23-Aug-26	16-Jan-27	21-Jan-27	$12,064.76	$12,064.76	100%
Geotextile & Bedding		192	28-Jul-26	10-Sep-26	22-Jul-26 A	23-Mar-27	$225,176.28	$225,176.28	100%
Installation of geotextile lining and coarse sand bedding		192	28-Jul-26	10-Sep-26	22-Jul-26 A	23-Mar-27	$225,176.28	$225,176.28	100%
MOD-RCP-C	Compact and level bedding for Rainwater Collection Ponds Zone 2	17	22-Aug-26	10-Sep-26	17-Feb-27	23-Mar-27	$102,352.85	$102,352.85	100%
MOD-RCP-C	Place 500mm thick coarse sand bedding for Rainwater Collection Ponds Zone 2	21	28-Jul-26	22-Aug-26	22-Jul-26 A	17-Feb-27	$122,823.42	$122,823.42	100%
Concrete Structures		8	16-Sep-26	27-Sep-26	20-Sep-26 A	01-Apr-27	$32,702.46	$32,702.46	100%
Construction of pond slab, walls, vertical structures		8	16-Sep-26	27-Sep-26	20-Sep-26 A	01-Apr-27	$32,702.46	$32,702.46	100%
MOD-RCP-C	Install formwork and reinforcement for Rainwater Collection Ponds Zone 2	8	16-Sep-26	27-Sep-26	20-Sep-26 A	01-Apr-27	$32,702.46	$32,702.46	100%
Road Crossing Zone 2		159	22-Jan-26	07-Oct-26	31-Dec-26	27-Jul-27	1,644,651.2	$1,644,651.20	99.17%
uPVC Road Crossing Pipes		68	22-Jan-26	22-Jun-26	31-Dec-26	07-Apr-27	1,202,844.7	$1,202,844.75	100%
Installation of uPVC pipes of various diameters crossing roadways		68	22-Jan-26	22-Jun-26	31-Dec-26	07-Apr-27	1,202,844.7	$1,202,844.75	100%
MOD-ROC-F	Reinstatement of road surface for Road Crossing Zone 2	6	15-Jun-26	22-Jun-26	01-Apr-27	07-Apr-27	$30,071.12	$30,071.12	100%
MOD-ROC-F	Backfilling and compaction in layers for Road Crossing Zone 2	8	26-May-26	15-Jun-26	23-Mar-27	31-Mar-27	$60,142.24	$60,142.24	100%
MOD-ROC-F	Testing of installed pipeline for Road Crossing Zone 2	6	19-May-26	26-May-26	16-Mar-27	22-Mar-27	$30,071.12	$30,071.12	100%
MOD-ROC-F	Placement of supports and protection around the pipe for Road Crossing Zone 2	5	07-May-26	19-May-26	02-Mar-27	15-Mar-27	$120,284.48	$120,284.48	100%
MOD-ROC-F	Laying of uPVC pipe (300mm, 315mm, 400mm, 600mm dia) for Road Crossing Zone 2	10	13-Apr-26	07-May-26	09-Feb-27	02-Mar-27	$481,137.90	$481,137.90	100%
MOD-ROC-F	Preparation of trench base with compacted bedding for Road Crossing Zone 2	5	26-Mar-26	13-Apr-26	02-Feb-27	09-Feb-27	$120,284.48	$120,284.48	100%
MOD-ROC-F	Excavation across road width to required depth for Road Crossing Zone 2	10	12-Feb-26	26-Mar-26	21-Jan-27	02-Feb-27	$180,426.71	$180,426.71	100%
MOD-ROC-F	Saw cutting and removal of asphalt (if applicable) for Road Crossing Zone 2	12	29-Jan-26	11-Feb-26	07-Jan-27	21-Jan-27	$120,284.48	$120,284.48	100%
MOD-ROC-F	Demarcation and traffic diversion (if required) for Road Crossing Zone 2	6	22-Jan-26	28-Jan-26	31-Dec-26	07-Jan-27	$60,142.24	$60,142.24	100%
GRP Road Crossing Pipes		91	22-Jun-26	07-Oct-26	08-Apr-27	27-Jul-27	$441,806.44	$441,806.44	96.92%
Installation of GRP pipes (800mm–1000mm dia) for road crossings		91	22-Jun-26	07-Oct-26	08-Apr-27	27-Jul-27	$441,806.44	$441,806.44	96.92%
MOD-ROC-C	Reinstate road surface (asphalt/concrete) for Road Crossing Zone 2	8	28-Sep-26	07-Oct-26	19-Jul-27	27-Jul-27	$22,656.74	$22,656.74	40%
MOD-ROC-C	Backfill and compact in layers for Road Crossing Zone 2	15	09-Sep-26	28-Sep-26	01-Jul-27	18-Jul-27	$45,313.48	$45,313.48	100%
MOD-ROC-C	Perform leak testing as per specifications for Road Crossing Zone 2	5	03-Sep-26	09-Sep-26	26-Jun-27	30-Jun-27	$11,328.37	$11,328.37	100%
MOD-ROC-C	Provide structural supports and closure at both ends for Road Crossing Zone 2	9	24-Aug-26	03-Sep-26	15-Jun-27	24-Jun-27	$45,313.48	$45,313.48	100%
MOD-ROC-C	Install GRP pipe (800mm & 1000mm dia) for Road Crossing Zone 2	21	30-Jul-26	24-Aug-26	22-May-27	14-Jun-27	$181,253.92	$181,253.92	100%
MOD-ROC-C	Lay compacted granular bedding for Road Crossing Zone 2	16	12-Jul-26	30-Jul-26	28-Apr-27	20-May-27	$67,970.22	$67,970.22	100%
MOD-ROC-C	Excavate trench across road at designed depth for Road Crossing Zone 2	12	28-Jun-26	12-Jul-26	14-Apr-27	27-Apr-27	$45,313.48	$45,313.48	100%
MOD-ROC-C	Set out location and coordinate with road authority for Road Crossing Zone 2	5	22-Jun-26	28-Jun-26	08-Apr-27	13-Apr-27	$22,656.74	$22,656.74	100%
Zone 1		343	06-Nov-25	25-Oct-26	01-Jul-26 A	27-Jul-27	4,225,340.4	$4,225,340.40	83.45%
Sewerage Network Zone 1		95	06-Nov-25	25-Oct-26	03-Oct-26	05-Jan-27	2,162,489.7	$2,162,489.79	68.78%
Fittings and Valves		27	21-Dec-25	20-Jan-26	05-Oct-26	05-Nov-26	$61,422.41	$61,422.41	100%
MOD-SWN-FV-	Jointing & Piping Accessories Installation for Sewerage Network Zone 1	3	18-Jan-26	20-Jan-26	02-Nov-26	05-Nov-26	$6,142.24	$6,142.24	100%
MOD-SWN-FV-	Air Breather & Air Release Valves Installation for Sewerage Network Zone 1	10	06-Jan-26	17-Jan-26	21-Oct-26	02-Nov-26	$23,181.49	$23,181.49	100%
MOD-SWN-FV-	Drain Valves Installation for Sewerage Network Zone 1	4	01-Jan-26	05-Jan-26	17-Oct-26	21-Oct-26	$8,785.65	$8,785.65	100%
MOD-SWN-FV-	Gate Valves Installation for Sewerage Network Zone 1	4	28-Dec-25	31-Dec-25	12-Oct-26	17-Oct-26	$9,660.60	$9,660.60	100%

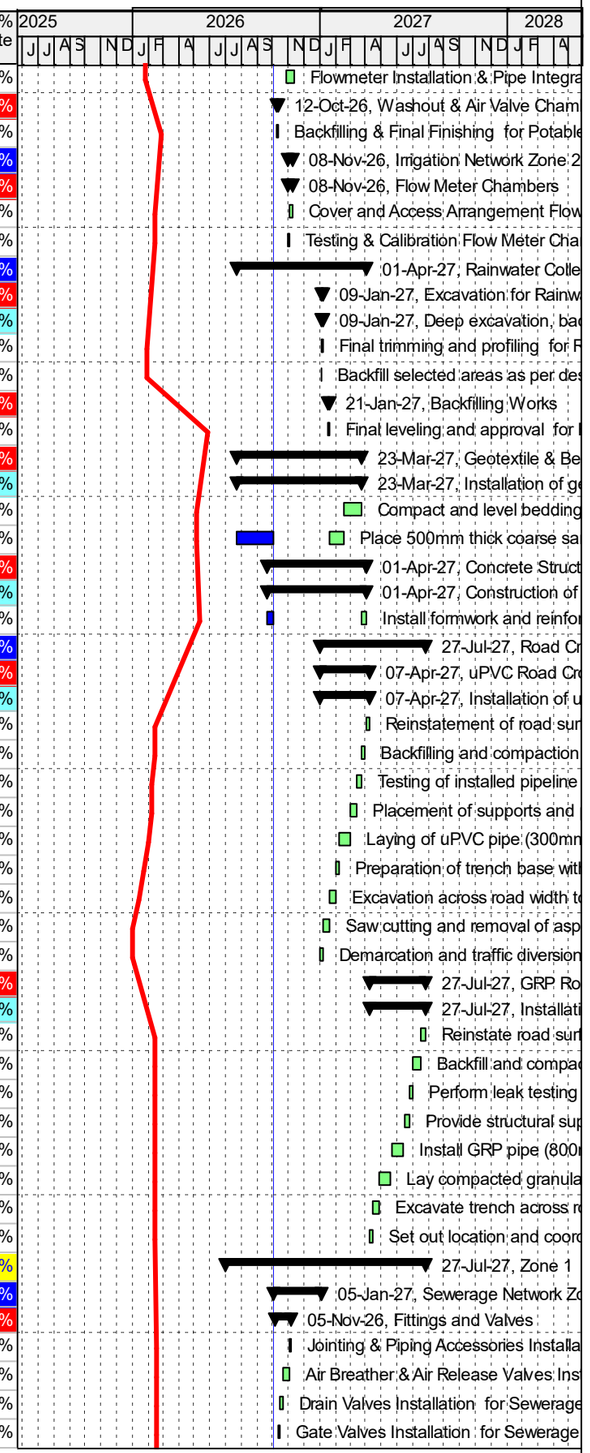


Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary

TASK filter: Activity % (Faiiled Start).

© Oracle Corporation

Development of Phase One – Part Two – Third Industrial

Activity ID	Activity Name	Original Duration	BL Project Start	BL Project Finish	Start	Finish	Budgeted Total Cost	Remaining Total Cost	Schedule % Complete
MOD-SWN-FV-	Supply & Installation of HDPE Elbows for Sewerage Network Zone 1	6	21-Dec-25	27-Dec-25	05-Oct-26	12-Oct-26	$13,652.43	$13,652.43	100%
Valve & Flow Meter Chambers		49	06-Dec-25	10-Feb-26	30-Oct-26	17-Dec-26	$25,475.78	$25,475.78	100%
Valve Chambers Construction		30	06-Dec-25	04-Jan-26	30-Oct-26	29-Nov-26	$4,136.44	$4,136.44	100%
MOD-SWN-	Test Valve Chamber for Sewerage Network Zone 1	15	06-Dec-25	20-Dec-25	30-Oct-26	14-Nov-26	$1,378.81	$1,378.81	100%
MOD-SWN-	Backfilling Valve Chamber for Sewerage Network Zone 1	15	21-Dec-25	04-Jan-26	14-Nov-26	29-Nov-26	$2,757.62	$2,757.62	100%
Water Drain Chambers Construction		15	09-Jan-26	23-Jan-26	12-Nov-26	27-Nov-26	$8,957.71	$8,957.71	100%
MOD-SWN-	Backfilling Water Drain Chamber for Sewerage Network Zone 1	15	09-Jan-26	23-Jan-26	12-Nov-26	27-Nov-26	$8,957.71	$8,957.71	100%
Discharge Chambers Construction		30	07-Jan-26	05-Feb-26	16-Nov-26	15-Dec-26	$9,386.17	$9,386.17	100%
MOD-SWN-	Test Discharge Chamber for Sewerage Network Zone 1	15	07-Jan-26	21-Jan-26	16-Nov-26	30-Nov-26	$3,128.72	$3,128.72	100%
MOD-SWN-	Backfilling Discharge Chamber for Sewerage Network Zone 1	15	22-Jan-26	05-Feb-26	01-Dec-26	15-Dec-26	$6,257.45	$6,257.45	100%
Flow Meter Chambers Construction		30	12-Jan-26	10-Feb-26	18-Nov-26	17-Dec-26	$2,995.46	$2,995.46	100%
MOD-SWN-	Test Flow Meter Chamber for Sewerage Network Zone 1	15	12-Jan-26	26-Jan-26	18-Nov-26	02-Dec-26	$998.49	$998.49	100%
MOD-SWN-	Backfilling Flow Meter Chamber for Sewerage Network Zone 1	15	27-Jan-26	10-Feb-26	03-Dec-26	17-Dec-26	$1,996.98	$1,996.98	100%
Manholes		20	05-Dec-25	08-Jan-26	04-Oct-26	24-Oct-26	$509,511.41	$509,511.41	100%
1200mm GRP Manholes with Backdrop		20	05-Dec-25	24-Dec-25	04-Oct-26	24-Oct-26	$253,577.48	$253,577.48	100%
MOD-SWN-	Test 1.2m GRP for Sewerage Network Zone 1	5	05-Dec-25	09-Dec-25	04-Oct-26	09-Oct-26	$84,525.83	$84,525.83	100%
MOD-SWN-	Backfilling 1.2m GRP for Sewerage Network Zone 1	15	10-Dec-25	24-Dec-25	09-Oct-26	24-Oct-26	$169,051.65	$169,051.65	100%
1500mm GRP Manholes (Standard & Backdrop)		20	10-Dec-25	29-Dec-25	04-Oct-26	24-Oct-26	$240,158.92	$240,158.92	100%
MOD-SWN-	Test 1.5m GRP for Sewerage Network Zone 1	5	10-Dec-25	14-Dec-25	04-Oct-26	09-Oct-26	$80,052.97	$80,052.97	100%
MOD-SWN-	Backfilling 1.5m GRP for Sewerage Network Zone 1	15	15-Dec-25	29-Dec-25	09-Oct-26	24-Oct-26	$160,105.94	$160,105.94	100%
1800mm GRP Manholes (Standard & Backdrop)		20	11-Dec-25	30-Dec-25	04-Oct-26	24-Oct-26	$11,980.90	$11,980.90	100%
MOD-SWN-	Test 1.8m GRP for Sewerage Network Zone 1	5	11-Dec-25	15-Dec-25	04-Oct-26	09-Oct-26	$3,993.63	$3,993.63	100%
MOD-SWN-	Backfilling 1.8m GRP for Sewerage Network Zone 1	15	16-Dec-25	30-Dec-25	09-Oct-26	24-Oct-26	$7,987.27	$7,987.27	100%
2000mm GRP Manholes (Standard & Backdrop)		20	20-Dec-25	08-Jan-26	04-Oct-26	24-Oct-26	$3,794.11	$3,794.11	100%
MOD-SWN-	Test 2m GRP for Sewerage Network Zone 1	5	20-Dec-25	24-Dec-25	04-Oct-26	09-Oct-26	$1,264.70	$1,264.70	100%
MOD-SWN-	Backfilling 2m GRP for Sewerage Network Zone 1	15	25-Dec-25	08-Jan-26	09-Oct-26	24-Oct-26	$2,529.41	$2,529.41	100%
Pumping Stations		82	06-Nov-25	25-Oct-26	03-Oct-26	05-Jan-27	1,566,080.2	$1,566,080.20	56.89%
Odor Control System		25	31-Aug-26	25-Oct-26	30-Nov-26	29-Dec-26	$276,510.51	$276,510.51	56.96%
MOD-SWN-	Odor control system – All stations (PS2) for Sewerage Network Zone 1	15	28-Sep-26	25-Oct-26	12-Dec-26	29-Dec-26	$138,255.26	$138,255.26	13.91%
MOD-SWN-	Odor control system – All stations (PS1) for Sewerage Network Zone 1	10	31-Aug-26	28-Sep-26	30-Nov-26	12-Dec-26	$138,255.26	$138,255.26	100%
In-Line Booster Stations		21	28-Sep-26	22-Oct-26	12-Dec-26	05-Jan-27	$656,073.36	$656,073.36	15.24%
MOD-SWN-	In-Line Booster Stations - Civil Works for Sewerage Network Zone 1	21	28-Sep-26	22-Oct-26	12-Dec-26	05-Jan-27	$656,073.36	$656,073.36	15.24%
Engine/Motor Control Center Buildings		8	06-Nov-25	08-Dec-25	03-Oct-26	11-Oct-26	$45,941.19	$45,941.19	100%
MOD-SWN-	MCC Building – PS2 for Sewerage Network Zone 1	7	01-Dec-25	08-Dec-25	04-Oct-26	11-Oct-26	$42,052.73	$42,052.73	100%
MOD-SWN-	MCC Building – PS1 for Sewerage Network Zone 1	1	06-Nov-25	06-Nov-25	03-Oct-26	03-Oct-26	$3,888.46	$3,888.46	100%
Valves and Fittings (General Supply & Installation)		5	18-Dec-25	23-Dec-25	29-Oct-26	04-Nov-26	$23,484.26	$23,484.26	100%
MOD-SWN-	Valves, fittings, flow meters – PS2 for Sewerage Network Zone 1	2	22-Dec-25	23-Dec-25	02-Nov-26	04-Nov-26	$11,924.59	$11,924.59	100%
MOD-SWN-	35mm raked bar SS 316 mesh – PS1 for Sewerage Network Zone 1	1	21-Dec-25	21-Dec-25	01-Nov-26	02-Nov-26	$4,838.91	$4,838.91	100%
MOD-SWN-	Valves, fittings & accessories – PS1 for Sewerage Network Zone 1	2	18-Dec-25	20-Dec-25	29-Oct-26	01-Nov-26	$6,720.76	$6,720.76	100%
Pump Well and Valve Chambers		62	19-Nov-25	29-Jan-26	04-Oct-26	14-Dec-26	$442,703.31	$442,703.31	100%
MOD-SWN-	Flow meter chamber – PS2 for Sewerage Network Zone 1	15	13-Jan-26	29-Jan-26	28-Nov-26	14-Dec-26	$90,972.17	$90,972.17	100%
MOD-SWN-	Valve chamber – PS2 for Sewerage Network Zone 1	16	25-Dec-25	12-Jan-26	09-Nov-26	26-Nov-26	$97,546.82	$97,546.82	100%
MOD-SWN-	Pump well & valve chamber structure – PS2 (2 wells, 3m each, 9m depth) for Sewerage	14	04-Dec-25	20-Dec-25	19-Oct-26	03-Nov-26	$81,656.84	$81,656.84	100%
MOD-SWN-	Flow meter chamber – PS1 for Sewerage Network Zone 1	4	21-Dec-25	24-Dec-25	04-Nov-26	08-Nov-26	$20,216.04	$20,216.04	100%
MOD-SWN-	Valve chamber – PS1 for Sewerage Network Zone 1	6	14-Dec-25	20-Dec-25	28-Oct-26	03-Nov-26	$34,141.39	$34,141.39	100%
MOD-SWN-	35 mm raked bar SS 316 network chamber PS1 for Sewerage Network Zone 1	1	13-Dec-25	13-Dec-25	27-Oct-26	27-Oct-26	$2,688.28	$2,688.28	100%
MOD-SWN-	Concrete wall (5x5x1m) inside PS1 well for Sewerage Network Zone 1	7	04-Dec-25	11-Dec-25	19-Oct-26	26-Oct-26	$41,284.68	$41,284.68	100%
MOD-SWN-	Pump well & valve chamber structure – PS1 (2 wells, 12m deep) for Sewerage Network	13	19-Nov-25	03-Dec-25	04-Oct-26	18-Oct-26	$74,197.09	$74,197.09	100%
Odor Control System Base/Plinth		6	25-Dec-25	31-Dec-25	25-Oct-26	31-Oct-26	$16,590.51	$16,590.51	100%
MOD-SWN-	Concrete plinth below odor control – All PSs for Sewerage Network Zone 1	6	25-Dec-25	31-Dec-25	25-Oct-26	31-Oct-26	$16,590.51	$16,590.51	100%

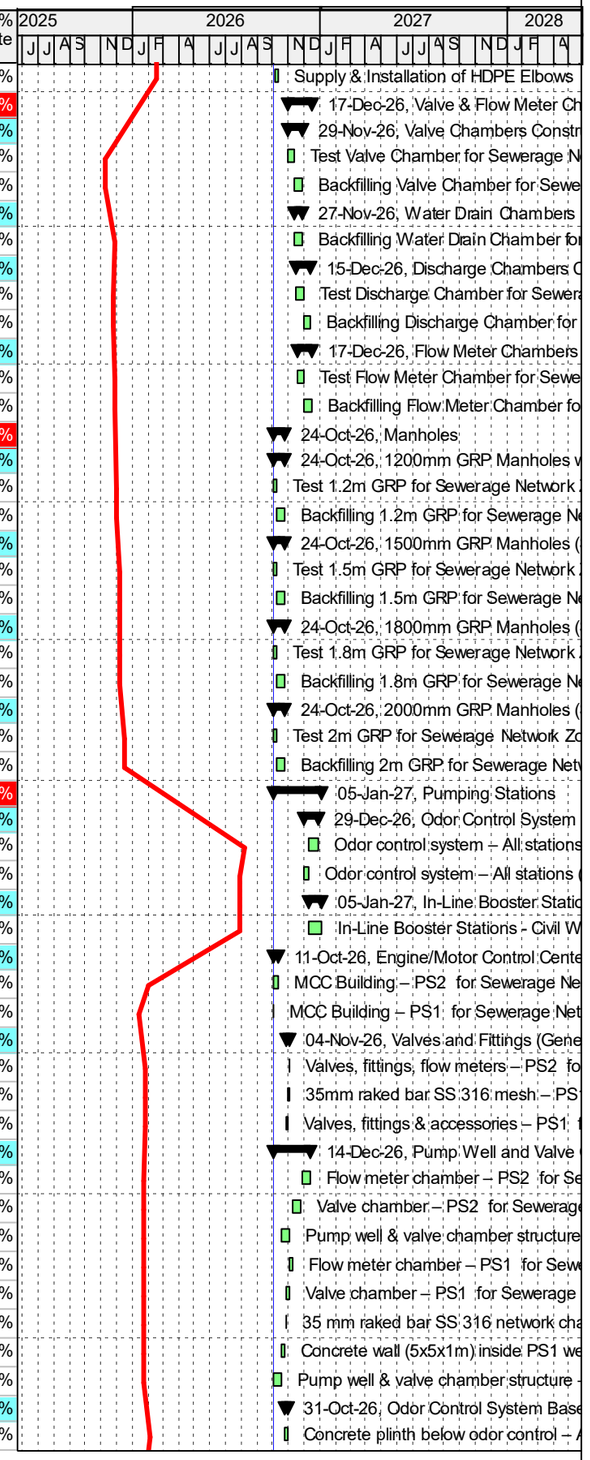


Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary

TASK filter: Activity % (Faiiled Start).

© Oracle Corporation

Development of Phase One – Part Two – Third Industrial

Activity ID	Activity Name	Original Duration	BL Project Start	BL Project Finish	Start	Finish	Budgeted Total Cost	Remaining Total Cost	Schedule % Complete
Duct Works		7	04-Dec-25	11-Dec-25	19-Oct-26	26-Oct-26	$15,220.07	$15,220.07	100%
MOD-SWN-	uPVC duct Track 8 – All PSs for Sewerage Network Zone 1	4	08-Dec-25	11-Dec-25	22-Oct-26	26-Oct-26	$9,274.58	$9,274.58	100%
MOD-SWN-	uPVC duct Track 2 – All PSs for Sewerage Network Zone 1	2	06-Dec-25	07-Dec-25	20-Oct-26	21-Oct-26	$3,185.08	$3,185.08	100%
MOD-SWN-	uPVC duct Track 1 – All PSs for Sewerage Network Zone 1	1	04-Dec-25	04-Dec-25	19-Oct-26	19-Oct-26	$2,760.41	$2,760.41	100%
Grounding Works		3	13-Dec-25	15-Dec-25	27-Oct-26	29-Oct-26	$7,603.32	$7,603.32	100%
MOD-SWN-	600x600 Cable pull pit – All PSs for Sewerage Network Zone 1	2	14-Dec-25	15-Dec-25	28-Oct-26	29-Oct-26	$5,913.15	$5,913.15	100%
MOD-SWN-	Grounding pit – Each PS for Sewerage Network Zone 1	1	13-Dec-25	13-Dec-25	27-Oct-26	27-Oct-26	$1,690.17	$1,690.17	100%
Landscaping / Interlocking Tiles		21	06-Dec-25	29-Dec-25	05-Oct-26	28-Oct-26	$61,674.68	$61,674.68	100%
MOD-SWN-	Entrance road paving tiles for Sewerage Network Zone 1	4	25-Dec-25	29-Dec-25	25-Oct-26	28-Oct-26	$10,721.87	$10,721.87	100%
MOD-SWN-	Building perimeter interlock tiles for Sewerage Network Zone 1	17	06-Dec-25	24-Dec-25	05-Oct-26	24-Oct-26	$50,952.81	$50,952.81	100%
Pumping Station Internal Drainage Network		7	01-Dec-25	08-Dec-25	03-Oct-26	10-Oct-26	$20,278.98	$20,278.98	100%
MOD-SWN-	Internal surface drainage channels for Sewerage Network Zone 1	7	01-Dec-25	08-Dec-25	03-Oct-26	10-Oct-26	$20,278.98	$20,278.98	100%
Rainwater Drainage Network Zone 1		25	02-Dec-25	18-Jan-26	04-Oct-26	02-Nov-26	$756,722.25	$756,722.25	100%
Precast Concrete Box Culverts		24	02-Dec-25	06-Jan-26	04-Oct-26	01-Nov-26	$272,670.30	$272,670.30	100%
Box Culverts (500x500mm to 3500x800mm)		13	17-Dec-25	06-Jan-26	12-Oct-26	27-Oct-26	$243,808.08	$243,808.08	100%
MOD-RWN-	Surface finishing Box culvert for Rainwater Drainage Network Zone 1	3	04-Jan-26	06-Jan-26	24-Oct-26	27-Oct-26	$63,602.11	$63,602.11	100%
MOD-RWN-	Backfilling and compaction Box culvert for Rainwater Drainage Network Zone 1	5	27-Dec-25	03-Jan-26	18-Oct-26	24-Oct-26	$74,202.46	$74,202.46	100%
MOD-RWN-	Construct headwalls/wing walls (if needed) Box culvert for Rainwater Drainage Network Zo	5	17-Dec-25	25-Dec-25	12-Oct-26	18-Oct-26	$106,003.51	$106,003.51	100%
Tube Culverts at Road Intersections		8	25-Dec-25	04-Jan-26	12-Oct-26	21-Oct-26	$17,897.63	$17,897.63	100%
MOD-RWN-	Backfilling and road reinstatement Tube culvert for Rainwater Drainage Network Zone 1	8	25-Dec-25	04-Jan-26	12-Oct-26	21-Oct-26	$17,897.63	$17,897.63	100%
Box Culverts at Road Intersections		24	02-Dec-25	01-Jan-26	04-Oct-26	01-Nov-26	$10,964.60	$10,964.60	100%
MOD-RWN-	Backfilling and surface reinstatement for Rainwater Drainage Network Zone 1	9	22-Dec-25	01-Jan-26	21-Oct-26	01-Nov-26	$216.41	$216.41	100%
MOD-RWN-	Joint treatment and testing for Rainwater Drainage Network Zone 1	10	08-Dec-25	22-Dec-25	10-Oct-26	21-Oct-26	$288.54	$288.54	100%
MOD-RWN-	Construct connection chambers (if needed) for Rainwater Drainage Network Zone 1	1	07-Dec-25	08-Dec-25	08-Oct-26	10-Oct-26	$1,082.03	$1,082.03	100%
MOD-RWN-	Install precast box culvert for Rainwater Drainage Network Zone 1	4	02-Dec-25	07-Dec-25	04-Oct-26	08-Oct-26	$9,377.62	$9,377.62	100%
Manholes		11	05-Jan-26	17-Jan-26	20-Oct-26	02-Nov-26	$24,412.88	$24,412.88	100%
Concrete Manholes for 1500x1500 Box Pipes		5	12-Jan-26	17-Jan-26	20-Oct-26	26-Oct-26	$10,635.13	$10,635.13	100%
MOD-RWN-	Backfill in layers Concrete Manhole 1.5x1.5 for Rainwater Drainage Network Zone 1	5	12-Jan-26	17-Jan-26	20-Oct-26	26-Oct-26	$10,635.13	$10,635.13	100%
Concrete Manholes for 1000x1000 Box Pipes		7	05-Jan-26	12-Jan-26	25-Oct-26	02-Nov-26	$13,777.76	$13,777.76	100%
MOD-RWN-	Backfill in layers Concrete Manhole 1x1 for Rainwater Drainage Network Zone 1	3	10-Jan-26	12-Jan-26	29-Oct-26	02-Nov-26	$5,904.75	$5,904.75	100%
MOD-RWN-	Install cover and frame Concrete Manhole 1x1 for Rainwater Drainage Network Zone 1	4	05-Jan-26	08-Jan-26	25-Oct-26	29-Oct-26	$7,873.00	$7,873.00	100%
Backfilling & Bedding		12	05-Jan-26	18-Jan-26	05-Oct-26	19-Oct-26	$459,639.06	$459,639.06	100%
Backfilling Materials (Type A– 201–700mm Pipes)		6	12-Jan-26	18-Jan-26	06-Oct-26	13-Oct-26	$306,675.71	$306,675.71	100%
MOD-RWN-	Final fill to subgrade level for Rainwater Drainage Network Zone 1	6	12-Jan-26	18-Jan-26	06-Oct-26	13-Oct-26	$306,675.71	$306,675.71	100%
Gravel Bedding & Filter Cloth for uPVC Drain Pipes		12	05-Jan-26	18-Jan-26	05-Oct-26	19-Oct-26	$152,963.36	$152,963.36	100%
MOD-RWN-	Final fill and trench restoration for Rainwater Drainage Network Zone 1	12	05-Jan-26	18-Jan-26	05-Oct-26	19-Oct-26	$152,963.36	$152,963.36	100%
Potable Water Network Zone 1		47	18-Dec-25	17-Jan-26	04-Oct-26	29-Nov-26	$138,256.29	$138,256.29	100%
Valve Installation & Chambers		2	25-Dec-25	27-Dec-25	04-Oct-26	06-Oct-26	$31,630.34	$31,630.34	100%
MOD-PWN-VC	Tagging & Painting for Potable Water Network Zone 1	2	25-Dec-25	27-Dec-25	04-Oct-26	06-Oct-26	$31,630.34	$31,630.34	100%
Flow Meter Installation		26	18-Dec-25	17-Jan-26	29-Oct-26	29-Nov-26	$67,689.77	$67,689.77	100%
MOD-PWN-FM	Calibration & Commissioning for Potable Water Network Zone 1	3	14-Jan-26	17-Jan-26	25-Nov-26	29-Nov-26	$6,153.62	$6,153.62	100%
MOD-PWN-FM	Wiring/Cabling if applicable for Potable Water Network Zone 1	8	05-Jan-26	13-Jan-26	16-Nov-26	25-Nov-26	$18,460.85	$18,460.85	100%
MOD-PWN-FM	Flowmeter Installation & Pipe Integration for Potable Water Network Zone 1	15	18-Dec-25	04-Jan-26	29-Oct-26	16-Nov-26	$43,075.31	$43,075.31	100%
Washout & Air Valve Chambers		3	04-Jan-26	06-Jan-26	10-Oct-26	13-Oct-26	$38,936.18	$38,936.18	100%
MOD-PWN-WA	Backfilling & Final Finishing for Potable Water Network Zone 1	3	04-Jan-26	06-Jan-26	10-Oct-26	13-Oct-26	$38,936.18	$38,936.18	100%
Irrigation Network Zone 1		70	06-Jan-26	18-Jan-26	01-Jul-26 A	09-Nov-26	$49,321.04	$49,321.04	100%
Flow Meter Chambers		70	06-Jan-26	18-Jan-26	01-Jul-26 A	09-Nov-26	$49,321.04	$49,321.04	100%
MOD-IRN-FC-0	Cover and Access Arrangement Flow Meter Chamber for Irrigation Network Zone 1	1	18-Jan-26	18-Jan-26	08-Nov-26	09-Nov-26	$4,483.73	$4,483.73	100%
MOD-IRN-FC-0	Testing & Calibration Flow Meter Chamber for Irrigation Network Zone 1	2	15-Jan-26	17-Jan-26	05-Nov-26	08-Nov-26	$13,451.19	$13,451.19	100%
MOD-IRN-FC-0	Flow Meter Installation (280, 300, 500 mm) Flow Meter Chamber for Irrigation Network Zo	6	06-Jan-26	12-Jan-26	01-Jul-26 A	05-Nov-26	$31,386.12	$31,386.12	100%
Rainwater Collection Ponds Zone 1		4	07-Mar-26	14-Mar-26	04-Jan-27	09-Jan-27	$5,919.63	$5,919.63	100%

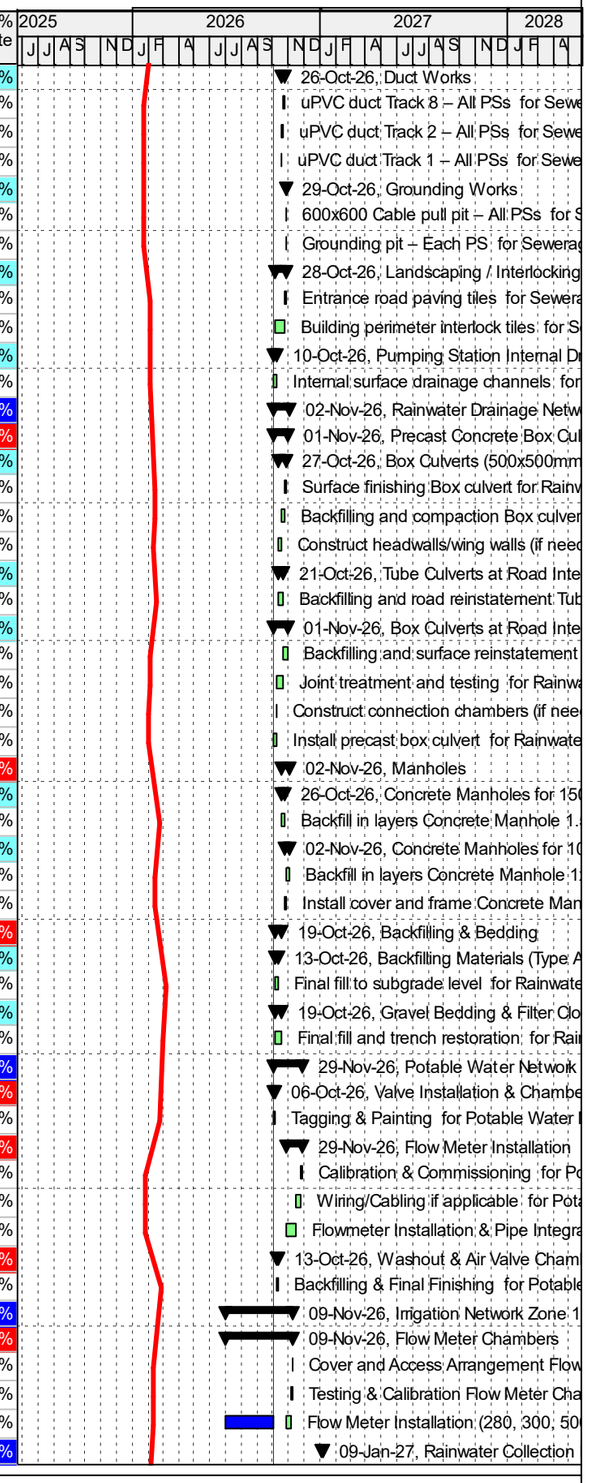


Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary

TASK filter: Activity % (Faiiled Start).

© Oracle Corporation

Development of Phase One – Part Two – Third Industrial

Activity ID	Activity Name	Original Duration	BL Project Start	BL Project Finish	Start	Finish	Budgeted Total Cost	Remaining Total Cost	Schedule % Complete
Excavation for Rainwater Drainage Pond		4	07-Mar-26	14-Mar-26	04-Jan-27	09-Jan-27	$5,919.63	$5,919.63	100%
Deep excavation, backfill, disposal for pond formation		4	07-Mar-26	14-Mar-26	04-Jan-27	09-Jan-27	$5,919.63	$5,919.63	100%
MOD-RCP-E	Final trimming and profiling for Rainwater Collection Ponds Zone 1	2	10-Mar-26	14-Mar-26	06-Jan-27	09-Jan-27	$2,536.98	$2,536.98	100%
MOD-RCP-E	Backfill selected areas as per design for Rainwater Collection Ponds Zone 1	2	07-Mar-26	10-Mar-26	04-Jan-27	06-Jan-27	$3,382.64	$3,382.64	100%
Road Crossing Zone 1		91	22-Jun-26	07-Oct-26	08-Apr-27	27-Jul-27	1,112,631.4	$1,112,631.40	97.84%
uPVC Road Crossing Pipes		91	22-Jun-26	07-Oct-26	08-Apr-27	27-Jul-27	1,112,631.4	$1,112,631.40	97.84%
Installation of uPVC pipes of various diameters crossing roadways		91	22-Jun-26	07-Oct-26	08-Apr-27	27-Jul-27	1,112,631.4	$1,112,631.40	97.84%
MOD-ROC-F	Testing of installed pipeline for Road Crossing Zone 1	6	30-Sep-26	07-Oct-26	21-Jul-27	27-Jul-27	$30,071.12	$30,071.12	20%
MOD-ROC-F	Placement of supports and protection around the pipe for Road Crossing Zone 1	10	17-Sep-26	30-Sep-26	10-Jul-27	20-Jul-27	$120,284.48	$120,284.48	100%
MOD-ROC-F	Laying of uPVC pipe (300mm, 315mm, 400mm, 600mm dia) for Road Crossing Zone 1	21	24-Aug-26	17-Sep-26	15-Jun-27	08-Jul-27	$481,137.90	$481,137.90	100%
MOD-ROC-F	Preparation of trench base with compacted bedding for Road Crossing Zone 1	15	06-Aug-26	24-Aug-26	29-May-27	14-Jun-27	$120,284.48	$120,284.48	100%
MOD-ROC-F	Excavation across road width to required depth for Road Crossing Zone 1	21	13-Jul-26	06-Aug-26	29-Apr-27	27-May-27	$180,426.71	$180,426.71	100%
MOD-ROC-F	Saw cutting and removal of asphalt (if applicable) for Road Crossing Zone 1	12	29-Jun-26	13-Jul-26	15-Apr-27	28-Apr-27	$120,284.48	$120,284.48	100%
MOD-ROC-F	Demarcation and traffic diversion (if required) for Road Crossing Zone 1	6	22-Jun-26	29-Jun-26	08-Apr-27	14-Apr-27	$60,142.24	$60,142.24	100%
General		91	07-May-26	11-Oct-26	16-Jan-27	24-May-27	1,403,713.4	$1,403,713.46	92.34%
Local Roads		4	29-Aug-26	02-Sep-26	10-Apr-27	14-Apr-27	$217.04	$217.04	100%
Bituminous Construction		4	29-Aug-26	02-Sep-26	10-Apr-27	14-Apr-27	$217.04	$217.04	100%
Bituminous Foundation Layer (MC 1)		4	29-Aug-26	02-Sep-26	10-Apr-27	14-Apr-27	$217.04	$217.04	100%
MOD-LOR-E	Prepare subgrade for Local Roads	4	29-Aug-26	02-Sep-26	10-Apr-27	14-Apr-27	$217.04	$217.04	100%
Arterial Roads		57	07-May-26	29-Aug-26	16-Jan-27	10-Apr-27	$155,149.71	$155,149.71	100%
Earthworks		2	07-May-26	10-May-26	16-Jan-27	18-Jan-27	$16,092.57	$16,092.57	100%
MOD-ARR-EW	Site Grading for Arterial Roads	1	09-May-26	10-May-26	17-Jan-27	18-Jan-27	$8,046.29	$8,046.29	100%
MOD-ARR-EW	Clear vegetation for Arterial Roads	1	07-May-26	09-May-26	16-Jan-27	17-Jan-27	$8,046.29	$8,046.29	100%
Precast Curbs (Type K1-D)		24	01-Aug-26	29-Aug-26	08-Mar-27	10-Apr-27	$139,057.14	$139,057.14	100%
MOD-ARR-PC-	Waste Disposal for Arterial Roads	8	19-Aug-26	29-Aug-26	31-Mar-27	10-Apr-27	$46,352.38	$46,352.38	100%
MOD-ARR-PC-	Finishing for Arterial Roads	8	10-Aug-26	19-Aug-26	22-Mar-27	31-Mar-27	$46,352.38	$46,352.38	100%
MOD-ARR-PC-	Backfilling & Compaction for Arterial Roads	8	01-Aug-26	10-Aug-26	08-Mar-27	22-Mar-27	$46,352.38	$46,352.38	100%
Communications		21	23-Aug-26	16-Sep-26	06-Mar-27	05-Apr-27	$583,011.57	$583,011.57	100%
Ductworks		21	23-Aug-26	16-Sep-26	06-Mar-27	05-Apr-27	$583,011.57	$583,011.57	100%
Concrete-Protected Service Culverts (50mm, 8 Outlets)		21	23-Aug-26	16-Sep-26	06-Mar-27	05-Apr-27	$583,011.57	$583,011.57	100%
MOD-COC-[	Testing & Restoration for Communications	21	23-Aug-26	16-Sep-26	06-Mar-27	05-Apr-27	$583,011.57	$583,011.57	100%
Landscape		62	29-Jul-26	11-Oct-26	28-Feb-27	24-May-27	$665,335.14	$665,335.14	83.85%
Supply & Planting of Trees and Shrubs		45	18-Aug-26	11-Oct-26	28-Mar-27	24-May-27	$578,701.17	$578,701.17	81.43%
planting of trees, shrubs, and vines		45	18-Aug-26	11-Oct-26	28-Mar-27	24-May-27	$578,701.17	$578,701.17	81.43%
MOD-LNS-F	Placement of sweet soil/potting soil as required for Landscape	21	15-Sep-26	11-Oct-26	25-Apr-27	24-May-27	$289,350.58	$289,350.58	62.86%
MOD-LNS-F	Excavation of planting pits as per specification for Landscape	16	27-Aug-26	15-Sep-26	06-Apr-27	25-Apr-27	$192,900.39	$192,900.39	100%
MOD-LNS-F	Site demarcation and marking of plant locations for Landscape	8	18-Aug-26	27-Aug-26	28-Mar-27	06-Apr-27	$96,450.19	$96,450.19	100%
Gravel Layer and Bed Preparation		37	29-Jul-26	10-Sep-26	28-Feb-27	20-Apr-27	$86,633.98	$86,633.98	100%
Installation of gravel layers and soil beds to support planting and drainage.		37	29-Jul-26	10-Sep-26	28-Feb-27	20-Apr-27	$86,633.98	$86,633.98	100%
MOD-LNS-C	Spreading of potting soil/sweet soil as top layer for Landscape	4	06-Sep-26	10-Sep-26	15-Apr-27	20-Apr-27	$10,829.25	$10,829.25	100%
MOD-LNS-C	Overlay of semi-permeable membrane (if applicable) for Landscape	4	01-Sep-26	06-Sep-26	11-Apr-27	15-Apr-27	$10,829.25	$10,829.25	100%
MOD-LNS-C	Spreading and compacting the gravel for Landscape	6	25-Aug-26	01-Sep-26	04-Apr-27	11-Apr-27	$12,995.10	$12,995.10	100%
MOD-LNS-C	Placement of 150mm gravel bed for drainage network for Landscape	6	18-Aug-26	25-Aug-26	28-Mar-27	04-Apr-27	$12,995.10	$12,995.10	100%
MOD-LNS-C	Placement of 50mm gravel layer for green areas for Landscape	10	06-Aug-26	18-Aug-26	16-Mar-27	28-Mar-27	$25,990.19	$25,990.19	100%
MOD-LNS-C	Excavation to required depth for Landscape	5	01-Aug-26	06-Aug-26	03-Mar-27	16-Mar-27	$8,663.40	$8,663.40	100%
MOD-LNS-C	Grading of planting areas for Landscape	2	29-Jul-26	01-Aug-26	28-Feb-27	03-Mar-27	$4,331.70	$4,331.70	100%

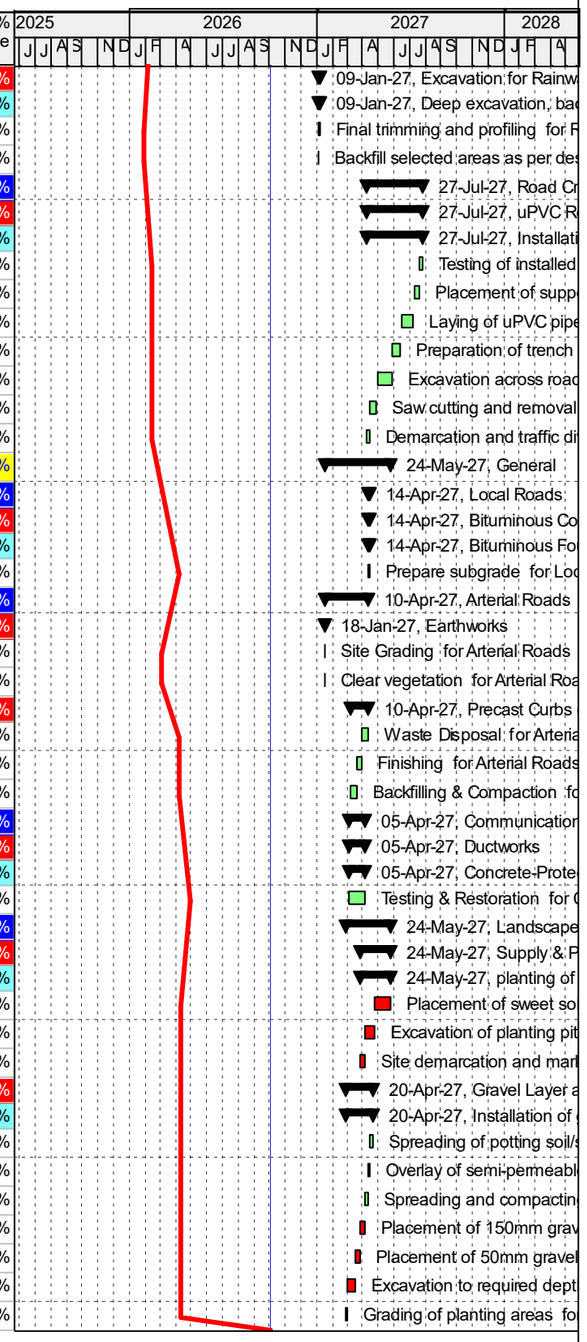

Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary

TASK filter: Activity % (Faiiled Start).

© Oracle Corporation
