
Activity ID	Activity Status	Activity Name	Planned Duration	BL Project Start	Start	BL Project Finish	Finish	Total Float	Performance % Complete	Schedule % Complete	Planned Total Cost	Earned Value Cost	Planned Value Cost	2025 Apr	2025 May
Modon Revised Schedule 01-Oct-26			654	19-May-25	19-May-25 A	18-May-27	25-Jun-27	-31	35.24%	42.86%	$234,303,968.75	$82,784,439.60	$100,677,118.28		
Part 02			654	19-May-2	19-May-25 A	18-May-27	25-Jun-27	-31	35.24%	42.86%	$234,303,968.75	$82,784,439.60	$100,677,118.28		
MileStones			654	19-May-2	19-May-25 A	18-May-27	25-Jun-27	-31	0%	0%	$0.00	$0.00	$0.00		
A1850	Completed	Project Start	0	19-May-2	19-May-25 A				100%	100%	$0.00	$0.00	$0.00		
A1860	Not Starte	Revised Scope Finish date	0			13-Feb-27	15-Apr-27*	-61	0%	0%	$0.00	$0.00	$0.00		
A1870	Not Starte	Saving Scope Finish date	0			18-May-27	25-Jun-27*	-37	0%	0%	$0.00	$0.00	$0.00		
A1880	Not Starte	Project Finish	0			18-May-27	25-Jun-27*	-37	0%	0%	$0.00	$0.00	$0.00		
A2350	Not Starte	T&C Finish Date	0			08-Mar-27	03-Apr-27*	-23	0%	0%	$0.00	$0.00	$0.00		
Revised Scope			635	19-May-2	19-May-25 A	13-Feb-27	15-Apr-27	35	50.43%	61.32%	$164,170,171.75	$82,784,439.60	$100,677,118.28		
Storm Network			386	03-Jan-26	03-Jan-26 A	28-Dec-26	30-Mar-27	50	65.16%	63.1%	$38,366,275.66	$25,000,165.16	$24,210,055.23		
A1910	In Progre:	UPVC	110	30-Jun-26	30-Jun-26 A	17-Oct-26	09-Nov-26	192	66%	86.36%	$2,603,162.65	$1,718,087.35	$2,248,185.92		
A1920	In Progre:	GRP Pipes	150	31-Jan-26	31-Jan-26 A	29-Jun-26	03-Nov-26	197	78.79%	100%	$104,418.07	$82,271.29	$104,418.07		
A1930	In Progre:	Box Culvert	160	18-Jul-26	18-Jul-26 A	25-Dec-26	04-Mar-27	-27	4.4%	47.81%	$2,840,078.63	$124,956.06	$1,357,912.59		
A1940	Not Starte	Pipes Culvert	113	21-Jul-26	03-Oct-26	28-Dec-26	23-Jan-27	-27	0%	45.78%	$0.00	$0.00	$0.00		
A1950	In Progre:	Manhoule	160	15-Jul-26	15-Jul-26 A	21-Dec-26	05-Mar-27	75	4%	50%	$3,195,831.57	$127,833.26	$1,597,915.79		
A1960	In Progre:	Gully outfalls	110	14-Jul-26	14-Jul-26 A	31-Oct-26	29-Oct-26	106	75.6%	73.64%	$1,493,547.47	$1,129,127.54	$1,099,794.05		
A1970	In Progre:	Catch Basins	110	09-Jul-26	09-Jul-26 A	26-Oct-26	29-Oct-26	202	75.7%	78.18%	$2,089,199.59	$1,581,539.92	$1,633,374.22		
A1980	In Progre:	Swales	140	13-Jul-26	13-Jul-26 A	30-Nov-26	15-Nov-26	186	69%	58.39%	$1,596,669.61	$1,101,702.03	$932,341.00		
A1990	In Progre:	Drinage Champer	110	05-Jul-26	05-Jul-26 A	22-Oct-26	02-Nov-26	199	72.6%	81.82%	$1,212,475.66	$880,261.92	$992,025.54		
A2000	In Progre:	Bedding	250	03-Jan-26	03-Jan-26 A	09-Sep-26	30-Mar-27	50	79%	100%	$749,276.26	$591,928.25	$749,276.26		
A2010	In Progre:	Open UPVC drainage pipes	140	01-Jul-26	01-Jul-26 A	18-Nov-26	01-Nov-26	200	79%	66.61%	$9,248,559.15	$7,306,361.73	$6,160,201.01		
A2020	In Progre:	Beeding Open UPVC drainage pipes	140	30-Jun-26	30-Jun-26 A	16-Nov-26	05-Oct-26	226	98.2%	67.86%	$3,170,663.11	$3,113,572.30	$2,151,521.39		
A2030	In Progre:	Geotextile	140	11-Jul-26	11-Jul-26 A	28-Nov-26	05-Oct-26	226	98.2%	59.46%	$1,604,901.14	$1,576,003.36	$954,343.00		
A2040	In Progre:	Collection sump	160	15-Jul-26	15-Jul-26 A	21-Dec-26	24-Nov-26	176	67%	50%	$8,457,492.76	$5,666,520.15	$4,228,746.38		
Ponds			608	19-May-2	19-May-25 A	29-Nov-26	16-Jan-27	123	77.34%	93.24%	$20,207,136.62	$15,627,773.91	$18,840,509.96		
A2050	Completed	Clearnce	63	19-May-2	19-May-25 A	20-Jul-25	20-Jul-26 A		100%	100%	$1,624,219.53	$1,624,219.53	$1,624,219.53		
A2060	In Progre:	Excavation	120	26-May-2	26-May-26 A	22-Sep-26	15-Oct-26	216	89.37%	100%	$7,742,309.19	$6,919,285.59	$7,742,309.19		
A2070	In Progre:	Disposal Material	120	23-Jun-26	23-Jun-26 A	20-Oct-26	05-Oct-26	-3	98.27%	85%	$5,240,947.18	$5,150,322.47	$4,454,805.10		
A2080	In Progre:	Filter	60	17-May-2	11-Jul-26 A	15-Jul-26	09-Oct-26	223	89.31%	100%	$169,129.86	$151,048.23	$169,129.86		
A2090	In Progre:	HDPE geomembrane waterproofing	120	26-May-2	26-May-26 A	22-Sep-26	06-Nov-26	194	71%	100%	$1,093,100.67	$776,101.48	$1,093,100.67		
A2100	In Progre:	Siphon pipework	60	18-Mar-26	18-Mar-26 A	16-May-26	07-Oct-26	224	92%	100%	$243,239.15	$223,780.02	$243,239.15		
A2110	In Progre:	blinding & Walls Concerete	60	21-Jul-25	21-Jul-25 A	18-Sep-25	06-Oct-26	226	94.33%	100%	$35,955.49	$33,916.76	$35,955.49		
A2120	In Progre:	RAFT Concerete	60	19-Sep-25	19-Sep-25 A	17-Nov-25	05-Oct-26	227	95.98%	100%	$58,926.18	$56,556.86	$58,926.18		
A2130	In Progre:	Backfilling	60	18-Nov-2	25-Nov-25 A	16-Jan-26	25-Nov-26	175	10%	100%	$2,832,636.24	$283,263.62	$2,832,636.24		
A2140	In Progre:	Power Floating	60	17-Jan-26	17-Jan-26 A	17-Mar-26	11-Nov-26	189	34%	100%	$203,346.43	$69,137.79	$203,346.43		
A2150	In Progre:	Perimeter waterproof	120	04-Jun-26	04-Jun-26 A	01-Oct-26	22-Oct-26	74	84%	100%	$34,086.00	$28,632.24	$34,086.00		
A2160	Not Starte	Entrance Rood	40	21-Oct-26	08-Dec-26	29-Nov-26	16-Jan-27	27	0%	0%	$580,484.58	$0.00	$0.00		
A2380	In Progre:	Riprap	444	19-May-2	11-Jul-25 A	05-Aug-26	19-Nov-26	46	89.32%	100%	$348,756.12	$311,509.32	$348,756.12		
Sewage Network			406	24-Dec-2	24-Dec-25 A	18-Dec-26	28-Mar-27	50	22.19%	37.34%	$33,043,135.80	$7,331,771.62	$12,338,091.45		
A1320	In Progre:	UPVC Pipes	320	29-Dec-2	29-Dec-25 A	13-Nov-26	27-Feb-27	82	54%	86.88%	$224,744.59	$121,362.08	$195,246.86		
A1330	In Progre:	GRP Pipes	320	29-Dec-2	29-Dec-25 A	13-Nov-26	13-Jan-27	127	68%	86.88%	$38,007.00	$25,844.76	$33,018.58		
A1340	In Progre:	HDPE Pipes	320	29-Dec-2	29-Dec-25 A	13-Nov-26	09-Dec-26	162	79%	86.88%	$263,382.46	$208,072.14	$228,813.51		
A1350	In Progre:	HDPE Fitting	320	03-Jan-26	03-Jan-26 A	18-Nov-26	02-Mar-27	79	53%	85.31%	$32,276.72	$17,106.66	$27,536.08		
A1360	Not Starte	Valves	30	19-Nov-2	03-Oct-26	18-Dec-26	01-Nov-26	103	0%	0%	$248,557.35	$0.00	$0.00		
A1370	In Progre:	Valve Champer	38	06-Nov-2	30-Jul-26 A	13-Dec-26	01-Nov-26	100	22%	0%	$395,373.58	$86,986.52	$0.00		
A1380	In Progre:	Manhoule	200	20-Apr-26	20-Apr-26 A	05-Nov-26	20-Jan-27	113	45%	83%	$5,381,600.69	$2,421,720.31	$4,466,728.57		
A1390	In Progre:	Bedding	260	24-Dec-2	24-Dec-25 A	09-Sep-26	28-Mar-27	50	32%	100%	$152,150.73	$48,688.23	$152,150.73		
A1400	In Progre:	Thurst Block	30	19-Nov-2	30-Jul-26 A	18-Dec-26	28-Oct-26	26	16%	0%	$20,054.91	$3,208.79	$0.00		

Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary

TASK filter: All Activities

© Oracle Corporation

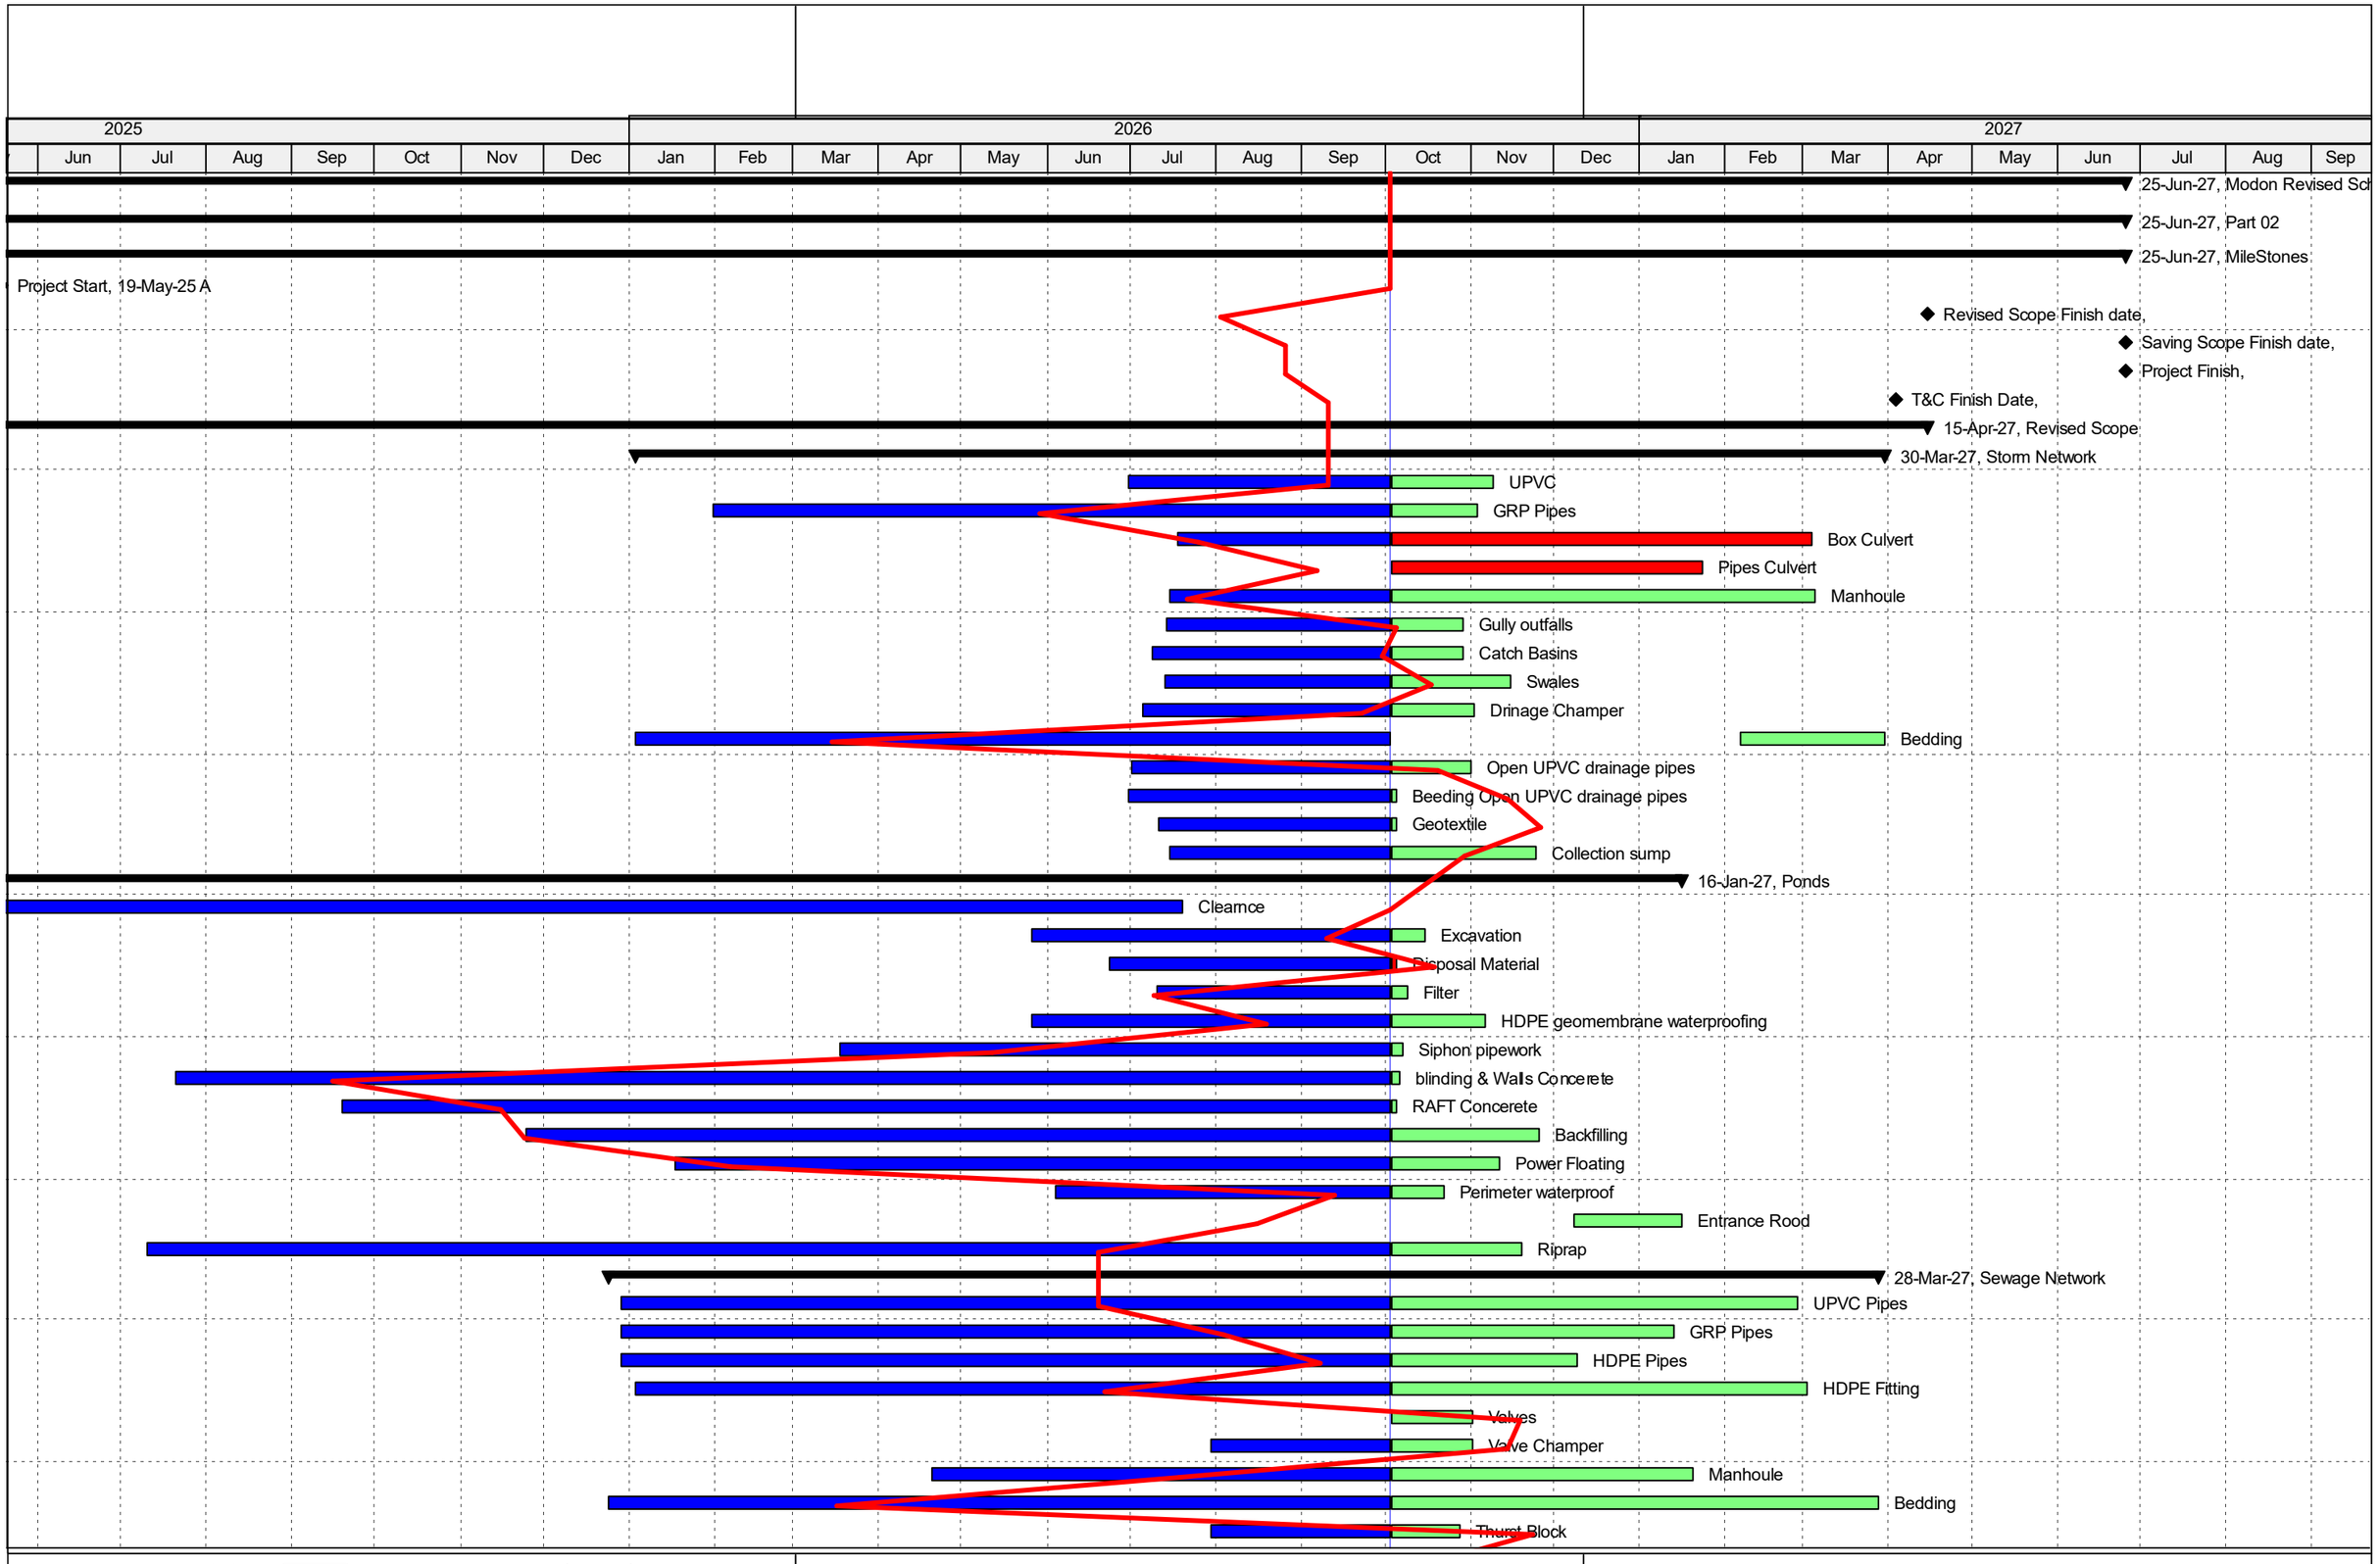

TASK filter: All Activities

© Oracle Corporation

Activity ID	Activity Status	Activity Name	Planned Duration	BL Project Start	Start	BL Project Finish	Finish	Total Float	Performance % Complete	Schedule % Complete	Planned Total Cost	Earned Value Cost	Planned Value Cost	2025 r	May
Pump Station (PS01)			203	16-May-2	16-May-26 A	15-Dec-26	04-Dec-26	166	10.86%	32.64%	$6,622,227.04	$719,246.02	$2,161,743.20		
A1	Not Starte	Pumps	15	23-Oct-26	09-Nov-26	07-Nov-26	24-Nov-26	166	0%	0%	$3,440,186.10	$0.00	$0.00		
A1	Not Starte	Odor System	60	15-Jul-26	03-Oct-26	13-Sep-26	01-Dec-26	169	0%	100%	$227,015.54	$0.00	$227,015.54		
A1	Not Starte	In-line Booste Station	10	07-Nov-2	24-Nov-26	17-Nov-26	04-Dec-26	166	0%	0%	$236,475.38	$0.00	$0.00		
A1	Not Starte	Raked bar SS 316 (35 mm)	15	08-Oct-26	25-Oct-26	23-Oct-26	09-Nov-26	166	0%	0%	$8,828.43	$0.00	$0.00		
A1	In Progres	Fual System Tank	25	13-Sep-26	30-Jul-26 A	08-Oct-26	25-Oct-26	166	9%	79%	$1,782,129.83	$160,391.68	$1,407,882.57		
A1	Not Starte	Concrete Element Works	60	15-Jul-26	03-Oct-26	13-Sep-26	01-Dec-26	169	0%	100%	$283,290.96	$0.00	$283,290.96		
A1	Completed	MCC Buildingn (Civil Work)	60	16-May-2	16-May-26 A	15-Jul-26	16-Aug-26 A		100%	100%	$243,554.13	$243,554.13	$243,554.13		
A1	Completed	Light Poles	15	17-Nov-2	30-Jul-26 A	02-Dec-26	19-Aug-26 A		100%	0%	$315,300.21	$315,300.21	$0.00		
A1	Not Starte	UPVC Ducts	15	08-Oct-26	25-Oct-26	23-Oct-26	09-Nov-26	176	0%	0%	$9,768.54	$0.00	$0.00		
A1	Not Starte	Earthing	15	23-Oct-26	09-Nov-26	07-Nov-26	24-Nov-26	176	0%	0%	$16,144.22	$0.00	$0.00		
A1	Not Starte	Interlock Paving	13	02-Dec-2	03-Oct-26	15-Dec-26	15-Oct-26	38	0%	0%	$59,533.70	$0.00	$0.00		
Pump Station (PS02)			323	17-Mar-26	17-Mar-26 A	13-Dec-26	16-Dec-26	154	22.24%	21.16%	$5,950,249.84	$1,323,289.79	$1,259,314.65		
A1	Not Starte	Pumps	15	11-Oct-26	02-Dec-26	26-Oct-26	16-Dec-26	154	0%	0%	$1,655,324.99	$0.00	$0.00		
A1	In Progres	Odor System	60	12-Aug-26	01-Sep-26 A	11-Oct-26	01-Nov-26	199	50%	86.25%	$227,015.54	$113,507.77	$195,800.90		
A1	In Progres	In-line Booste Station	25	26-Oct-26	31-Jul-26 A	20-Nov-26	26-Oct-26	205	5.5%	0%	$2,601,224.72	$143,067.36	$0.00		
A1	In Progres	Valves	15	26-Oct-26	25-Aug-27 A	10-Nov-26	09-Oct-26	19	56.5%	0%	$21,755.78	$12,292.01	$0.00		
A1	Completed	Entrance Gate	60	17-Mar-26	17-Mar-26 A	16-May-26	11-Jun-26 A		100%	100%	$53,600.37	$53,600.37	$53,600.37		
A1	In Progres	Concrete Element Works	60	17-Mar-26	17-Mar-26 A	16-May-26	13-Nov-26	187	30.1%	100%	$443,629.94	$133,535.69	$443,629.94		
A1	Completed	MCC Buildingn (Civil Work)	60	13-Jun-26	13-Jun-26 A	12-Aug-26	16-Aug-26 A		100%	100%	$551,986.37	$551,986.37	$551,986.37		
A1	Completed	Light Poles	23	26-Oct-26	30-Jul-26 A	18-Nov-26	19-Aug-26 A		100%	0%	$315,300.21	$315,300.21	$0.00		
A1	Not Starte	UPVC Ducts	30	12-Aug-26	03-Oct-26	11-Sep-26	01-Nov-26	154	0%	100%	$2,592.50	$0.00	$2,592.50		
A1	Not Starte	Earthing	30	11-Sep-26	02-Nov-26	11-Oct-26	01-Dec-26	154	0%	72.5%	$16,144.22	$0.00	$11,704.56		
A1	Not Starte	Interlock Paving	25	18-Nov-2	09-Oct-26	13-Dec-26	03-Nov-26	19	0%	0%	$61,675.20	$0.00	$0.00		
Pump Station (PS03)			258	16-May-2	19-May-26 A	15-Dec-26	01-Dec-26	169	16.26%	17.03%	$8,061,199.28	$1,311,044.56	$1,373,211.45		
A1	Not Starte	Pumps	15	28-Oct-26	17-Nov-26	12-Nov-26	01-Dec-26	169	0%	0%	$3,678,499.17	$0.00	$0.00		
A1	In Progres	Odor System	20	03-Sep-26	30-Aug-26 A	23-Sep-26	12-Oct-26	169	50%	100%	$227,015.54	$113,507.77	$227,015.54		
A1	In Progres	In-line Booste Station	20	12-Nov-2	30-Jul-26 A	02-Dec-26	21-Oct-26	19	5.5%	0%	$2,601,224.72	$143,067.36	$0.00		
A1	In Progres	Valves	15	12-Nov-2	23-Aug-27 A	27-Nov-26	09-Oct-26	222	56.6%	0%	$21,755.78	$12,313.17	$0.00		
A1	Not Starte	Entrance Gates	60	05-Jul-26	03-Oct-26	03-Sep-26	01-Dec-26	169	0%	100%	$30,898.91	$0.00	$30,898.91		
A1	In Progres	Concrete Element Works	60	05-Jul-26	05-Jul-26 A	03-Sep-26	05-Nov-26	169	44.8%	100%	$700,016.43	$313,597.64	$700,016.43		
A1	Completed	MCC Buildingn (Civil Work)	50	16-May-2	19-May-26 A	05-Jul-26	16-Aug-26 A		100%	100%	$413,258.42	$413,258.42	$413,258.42		
A1	Completed	Light Poles	10	02-Dec-2	30-Jul-26 A	12-Dec-26	20-Aug-26 A		100%	0%	$315,300.21	$315,300.21	$0.00		
A1	Not Starte	UPVC Ducts	20	23-Sep-26	13-Oct-26	13-Oct-26	01-Nov-26	169	0%	48.75%	$4,148.00	$0.00	$2,022.15		
A1	Not Starte	Earthing	15	13-Oct-26	02-Nov-26	28-Oct-26	16-Nov-26	169	0%	0%	$16,144.22	$0.00	$0.00		
A1	Not Starte	Interlock Paving	13	02-Dec-2	21-Oct-26	15-Dec-26	03-Nov-26	19	0%	0%	$52,937.88	$0.00	$0.00		
Pump Station (PS04)			250	14-Apr-26	14-Apr-26 A	09-Dec-26	14-Dec-26	156	18.49%	43.17%	$5,653,311.61	$1,045,201.74	$2,440,327.82		
A1	Not Starte	Pumps	15	22-Oct-26	14-Nov-26	06-Nov-26	29-Nov-26	162	0%	0%	$1,576,516.58	$0.00	$0.00		
A1	In Progres	Odor System	45	16-Jul-26	23-Aug-26 A	30-Aug-26	25-Oct-26	197	50%	100%	$227,015.54	$113,507.77	$227,015.54		
A1	Not Starte	In-line Booste Station	10	06-Nov-2	29-Nov-26	16-Nov-26	09-Dec-26	162	0%	0%	$1,024,724.56	$0.00	$0.00		
A1	In Progres	Valves	10	06-Nov-2	26-Aug-26 A	16-Nov-26	08-Oct-26	32	46.4%	0%	$26,485.29	$12,288.07	$0.00		
A1	Not Starte	Raked bar SS 316 (35 mm)	15	07-Oct-26	30-Oct-26	22-Oct-26	14-Nov-26	162	0%	0%	$31,530.11	$0.00	$0.00		
A1	Not Starte	Concrete Element Works	60	09-Jul-26	16-Oct-26	07-Sep-26	14-Dec-26	156	0%	100%	$537,725.08	$0.00	$537,725.08		
A1	In Progres	MCC Buildingn (Civil Work)	60	17-May-2	17-May-26 A	16-Jul-26	03-Oct-26	199	99.4%	100%	$450,721.62	$448,014.16	$450,721.62		
A1	Completed	Light Poles	10	16-Nov-2	30-Jul-26 A	26-Nov-26	25-Aug-26 A		100%	0%	$315,300.21	$315,300.21	$0.00		
A1	Not Starte	UPVC Ducts	15	07-Oct-26	30-Oct-26	22-Oct-26	14-Nov-26	172	0%	0%	$4,148.00	$0.00	$0.00		
A1	Not Starte	Earthing	15	22-Oct-26	14-Nov-26	06-Nov-26	29-Nov-26	172	0%	0%	$16,144.22	$0.00	$0.00		
A1	Not Starte	Interlock Paving	13	26-Nov-2	08-Oct-26	09-Dec-26	21-Oct-26	32	0%	0%	$21,072.36	$0.00	$0.00		

© Oracle Corporation

2025 | 2026 | 2027

Jun Jul Aug Sep Oct Nov Dec Jan Feb Mar Apr May Jun Jul Aug Sep Oct Nov Dec Jan Feb Mar Apr May Jun Jul Aug Sep

04-Dec-26, Pump Station (PS01)
Pumps
Odor System
In-line Booste Station
Raked bar SS 316 (35 mm)
Fual System Tank
Concrete Element Works
MCC Buildingn (Civil Work)
Light Poles
UPVC Ducts
Earthing
Interlock Paving
16-Dec-26, Pump Station (PS02)
Pumps
Odor System
In-line Booste Station
Entrance Gate
Concrete Element Works
MCC Buildingn (Civil Work)
Light Poles
UPVC Ducts
Earthing
Interlock Paving
01-Dec-26, Pump Station (PS03)
Pumps
Odor System
In-line Booste Station
Entrance Gates
Concrete Element Works
MCC Buildingn (Civil Work)
Light Poles
UPVC Ducts
Earthing
Interlock Paving
14-Dec-26, Pump Station (PS04)
Pumps
Odor System
In-line Booste Station
Valves
Raked bar SS 316 (35 mm)
Concrete Element Works
MCC Buildingn (Civil Work)
Light Poles
UPVC Ducts
Earthing
Interlock Paving


Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary

TASK filter: All Activities

© Oracle Corporation

Activity ID	Activity Status	Activity Name	Planned Duration	BL Project Start	Start	BL Project Finish	Finish	Total Float	Performance % Complete	Schedule % Complete	Planned Total Cost	Earned Value Cost	Planned Value Cost	2025
														r May
A1	In Progre:	Fual System Tank	30	07-Sep-26	30-Jul-26 A	07-Oct-26	30-Oct-26	162	9%	85.83%	$1,391,029.13	$125,192.62	$1,193,966.67	
A1	Completed	Entrance Gates	30	14-Apr-26	14-Apr-26 A	14-May-26	22-Aug-26 A		100%	100%	$30,898.91	$30,898.91	$30,898.91	
Potable Water Network			417	23-Dec-2	23-Dec-25 A	31-Dec-26	13-Feb-27	96	46.37%	64.46%	$35,439,165.61	$16,434,350.92	$22,844,529.32	
A1100	In Progre:	HDPE Pipes	250	24-Dec-2	24-Dec-25 A	30-Aug-26	05-Nov-26	96	86.67%	100%	$1,851,709.67	$1,604,876.77	$1,851,709.67	
A1110	In Progre:	HDPE Fitting	150	15-Apr-26	15-Apr-26 A	11-Sep-26	04-Dec-26	166	58.2%	100%	$526,461.84	$306,400.79	$526,461.84	
A1120	In Progre:	Valves	165	16-Jun-26	16-Jun-26 A	28-Nov-26	06-Dec-26	165	61%	65.61%	$2,300,902.87	$1,403,550.75	$1,509,531.73	
A1130	In Progre:	Fire Hydrant	30	12-Sep-26	13-Jul-26 A	11-Oct-26	11-Oct-26	220	70%	70%	$3,870,516.78	$2,709,361.75	$2,709,361.75	
A1140	In Progre:	Valve Champer	15	12-Oct-26	03-Aug-26 A	26-Oct-26	14-Oct-26	32	23.81%	0%	$4,238,202.38	$1,008,927.62	$0.00	
A1150	In Progre:	Sand Bedding & Covr	220	23-Dec-2	23-Dec-25 A	31-Jul-26	12-Oct-26	220	95.8%	100%	$52,947.70	$50,724.00	$52,947.70	
A1160	In Progre:	Thrust Block	90	11-Jun-26	11-Jun-26 A	09-Sep-26	12-Nov-26	188	54.79%	100%	$627,441.38	$343,771.07	$627,441.38	
A1170	Not Starte	Fire Fighting Pump	10	30-Oct-26	04-Jan-27	08-Nov-26	14-Jan-27	96	0%	0%	$2,317,808.95	$0.00	$0.00	
A1180	Not Starte	Surge vessel Fual System Tank	20	09-Nov-2	14-Jan-27	28-Nov-26	03-Feb-27	96	0%	0%	$46,349.72	$0.00	$0.00	
A1190	Not Starte	Surge vessel Valve	10	29-Nov-2	03-Feb-27	08-Dec-26	13-Feb-27	96	0%	0%	$271,877.41	$0.00	$0.00	
A1200	Not Starte	Pump Building	60	31-Aug-26	05-Nov-26	29-Oct-26	04-Jan-27	96	0%	55%	$42,565.49	$0.00	$23,411.02	
A1210	In Progre:	Water Tank	200	12-Feb-26	12-Feb-26 A	30-Aug-26	05-Nov-26	96	83.93%	100%	$8,472,030.24	$7,110,592.63	$8,472,030.24	
A1220	In Progre:	Generator	149	14-Jun-26	14-Jun-26 A	09-Nov-26	13-Feb-27	96	10.5%	74.5%	$9,180,791.70	$964,034.48	$6,839,381.74	
A1230	In Progre:	Coloration System	23	09-Dec-2	10-Aug-26 A	31-Dec-26	08-Oct-26	51	75%	0%	$851,309.40	$638,482.05	$0.00	
A1240	In Progre:	Street Lighting	112	31-Aug-26	30-Jul-26 A	20-Dec-26	12-Dec-26	63	37.25%	29.46%	$788,250.08	$293,629.02	$232,252.26	
Irrigation Network			286	12-Feb-26	12-Feb-26 A	24-Nov-26	01-Feb-27	107	70.12%	87%	$5,492,965.01	$3,851,602.72	$4,778,634.89	
A1250	In Progre:	HDPE Pipes	210	22-Feb-26	22-Feb-26 A	19-Sep-26	28-Oct-26	203	87.8%	100%	$1,090,193.50	$957,185.57	$1,090,193.50	
A1260	In Progre:	HDPE Fitting	210	03-Mar-26	03-Mar-26 A	28-Sep-26	03-Jan-27	137	56%	100%	$489,595.58	$274,173.52	$489,595.58	
A1270	In Progre:	Valves	200	28-Apr-26	28-Apr-26 A	13-Nov-26	23-Nov-26	177	74%	79%	$1,357,806.30	$1,004,776.66	$1,072,666.98	
A1280	In Progre:	Valve Champer	140	04-Jun-26	04-Jun-26 A	21-Oct-26	16-Nov-26	88	68%	86.43%	$1,792,422.14	$1,218,847.06	$1,549,164.85	
A1290	In Progre:	Flow meter Valves	200	07-May-2	07-May-26 A	22-Nov-26	01-Feb-27	107	39.1%	74.5%	$365,474.57	$142,900.56	$272,278.55	
A1300	In Progre:	Bedding	170	12-Feb-26	12-Feb-26 A	31-Jul-26	16-Oct-26	215	92%	100%	$117,510.68	$108,109.83	$117,510.68	
A1310	In Progre:	Thrust Block	160	18-Jun-26	18-Jun-26 A	24-Nov-26	18-Dec-26	-27	52.01%	66.88%	$279,962.24	$145,609.53	$187,224.75	
Road Crossing			160	18-Mar-26	18-Mar-26 A	24-Aug-26	07-Dec-26	27	58.75%	100%	$1,094,032.78	$642,744.26	$1,094,032.78	
A2170	In Progre:	Rood Crossing UPVC Selves	160	18-Mar-26	18-Mar-26 A	24-Aug-26	07-Dec-26	27	58.75%	100%	$1,094,032.78	$642,744.26	$1,094,032.78	
Road Works			90	27-Oct-26	31-Oct-26	10-Dec-26	28-Jan-27	15	0%	0%	$137,924.77	$0.00	$0.00	
A1030	Not Starte	MC1	20	27-Oct-26	31-Oct-26*	05-Nov-26	19-Nov-26	15	0%	0%	$769.77	$0.00	$0.00	
A1040	Not Starte	Binder Course	20	06-Nov-2	20-Nov-26	15-Nov-26	09-Dec-26	15	0%	0%	$46,800.49	$0.00	$0.00	
A1050	Not Starte	Wearing Couse	20	16-Nov-2	10-Dec-26	27-Nov-26	29-Dec-26	15	0%	0%	$73,203.97	$0.00	$0.00	
A1060	Not Starte	Pre-Cast Cerb	30	28-Nov-2	30-Dec-26	10-Dec-26	28-Jan-27	15	0%	0%	$17,150.53	$0.00	$0.00	
Hard Scape (Curbstone)			120	06-Aug-26	06-Aug-26 A	03-Dec-26	17-Jan-27	27	11.6%	48.33%	$763,034.65	$88,517.32	$368,800.08	
A1020	In Progre:	Pre-Cast Cerb	120	06-Aug-26	06-Aug-26 A	03-Dec-26	17-Jan-27	27	11.6%	48.33%	$763,034.65	$88,517.32	$368,800.08	
Secondary Irrigation Network			72	21-Oct-26	08-Nov-26	31-Dec-26	18-Jan-27	-37	0%	0%	$7,881,615.06	$0.00	$0.00	
A2180	Not Starte	Phoenix Dactylifera	15	30-Nov-2	18-Dec-26	14-Dec-26	02-Jan-27	-37	0%	0%	$2,549,692.23	$0.00	$0.00	
A2190	Not Starte	Shrubs and Vines,	15	30-Nov-2	18-Dec-26	14-Dec-26	02-Jan-27	-37	0%	0%	$0.00	$0.00	$0.00	
A2200	Not Starte	Peltophorum Inerme	15	30-Nov-2	18-Dec-26	14-Dec-26	02-Jan-27	-37	0%	0%	$572,037.93	$0.00	$0.00	
A2210	Not Starte	Atriplex canescens	15	30-Nov-2	18-Dec-26	14-Dec-26	02-Jan-27	-37	0%	0%	$45,446.21	$0.00	$0.00	
A2220	Not Starte	Gravel 150 mm	10	05-Nov-2	23-Nov-26	14-Nov-26	03-Dec-26	-37	0%	0%	$41,338.14	$0.00	$0.00	
A2240	Not Starte	Clean Sand	16	21-Oct-26	08-Nov-26*	04-Nov-26	23-Nov-26	-37	0%	0%	$100,784.36	$0.00	$0.00	
A2250	Not Starte	Irrigation System	15	15-Nov-2	03-Dec-26	29-Nov-26	18-Dec-26	-37	0%	0%	$2,696,877.35	$0.00	$0.00	
A2260	Not Starte	Maintance	16	15-Dec-2	02-Jan-27	31-Dec-26	18-Jan-27	-37	0%	0%	$1,875,438.84	$0.00	$0.00	
Telecom			417	23-Dec-2	23-Dec-25 A	13-Feb-27	15-Apr-27	35	63.5%	74.51%	$21,744,885.79	$13,807,513.70	$16,202,464.57	
A1070	In Progre:	Duct Bank	360	17-Feb-26	17-Feb-26 A	12-Feb-27	15-Apr-27	-61	46%	63.26%	$13,861,818.71	$6,376,436.61	$8,769,525.59	
A1080	In Progre:	Road Crossing	361	17-Feb-26	17-Feb-26 A	13-Feb-27	11-Nov-26	93	89%	63.09%	$1,219,484.00	$1,085,339.35	$769,355.90	
A1090	In Progre:	Manhole	220	23-Dec-2	23-Dec-25 A	31-Jul-26	13-Oct-26	219	95.23%	100%	$6,663,583.08	$6,345,737.74	$6,663,583.08	
Testing & Comissioning			157	24-Nov-2	03-Oct-26	06-Mar-27	03-Apr-27	-23	0%	0%	$0.00	$0.00	$0.00	

© Oracle Corporation

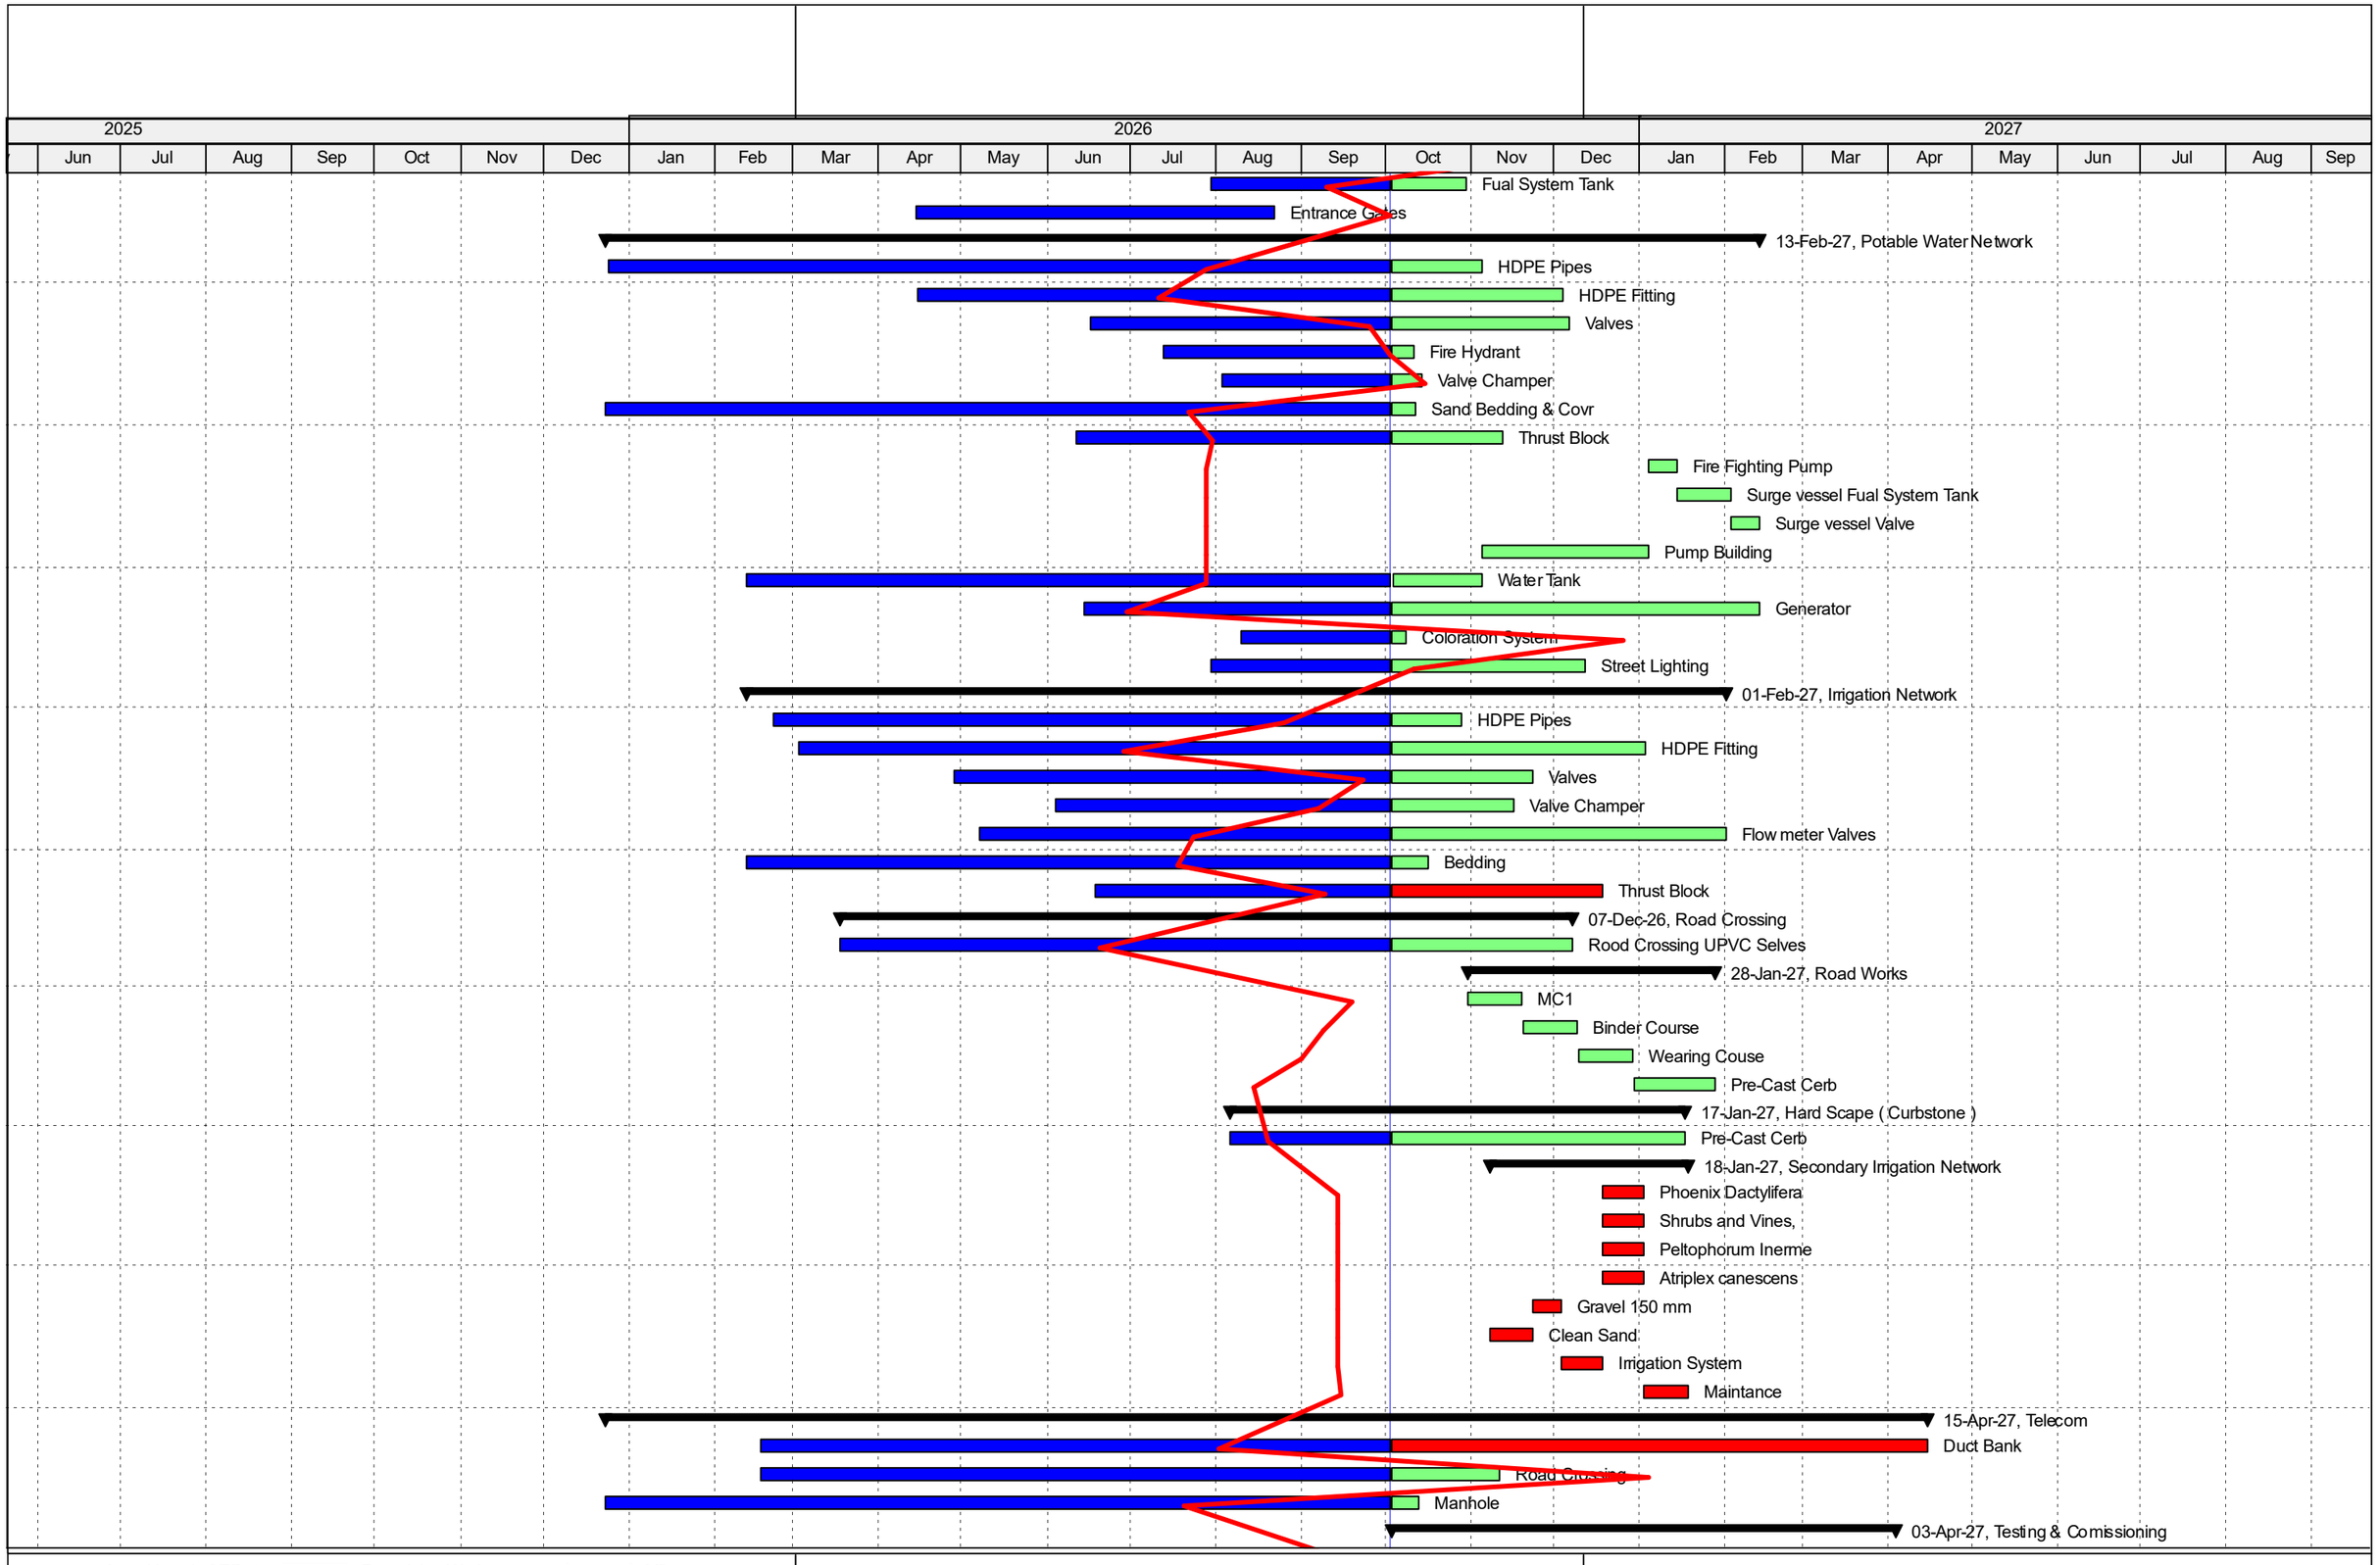


TASK filter: All Activities

© Oracle Corporation

Activity ID	Activity Status	Activity Name	Planned Duration	BL Project Start	Start	BL Project Finish	Finish	Total Float	Performance % Complete	Schedule % Complete	Planned Total Cost	Earned Value Cost	Planned Value Cost	2025
														r May
A2230	Not Starte	Potable Water T&C	90	09-Dec-2	03-Oct-26	31-Dec-26	14-Jan-27	44	0%	0%	$0.00	$0.00	$0.00	
A2340	Not Starte	Lateral Irrigation Network T&C	91	24-Nov-2	19-Dec-26	02-Feb-27	03-Apr-27	-23	0%	0%	$0.00	$0.00	$0.00	
A2360	Not Starte	Seweage Testing & Comissiong	90	19-Dec-2	03-Nov-26	31-Dec-26	16-Feb-27	16	0%	0%	$0.00	$0.00	$0.00	
A2370	Not Starte	Drainage Network T&C	60	28-Dec-2	23-Jan-27	06-Mar-27	03-Apr-27	-23	0%	0%	$0.00	$0.00	$0.00	
Saving Scope			158	01-Jan-27	18-Jan-27	18-May-27	25-Jun-27	-37	0%	0%	$70,133,797.00	$0.00	$0.00	
General Works			30	01-Jan-27	18-Jan-27	30-Jan-27	17-Feb-27	-37	0%	0%	$1,386,106.41	$0.00	$0.00	
A2280	Not Starte	Saving Works	30	01-Jan-27	18-Jan-27	30-Jan-27	17-Feb-27	-37	0%	0%	$1,386,106.41	$0.00	$0.00	
Local Road			15	31-Jan-27	17-Feb-27	14-Feb-27	04-Mar-27	-37	0%	0%	$779,435.79	$0.00	$0.00	
A2290	Not Starte	Saving Works	15	31-Jan-27	17-Feb-27	14-Feb-27	04-Mar-27	-37	0%	0%	$779,435.79	$0.00	$0.00	
Lateral Irrigation Network			45	15-Feb-27	04-Mar-27	31-Mar-27	18-Apr-27	-37	0%	0%	$1,314,624.27	$0.00	$0.00	
A2300	Not Starte	Saving Works	45	15-Feb-27	04-Mar-27	31-Mar-27	18-Apr-27	-37	0%	0%	$1,314,624.27	$0.00	$0.00	
Drainage Network			49	01-Apr-27	18-Apr-27	18-May-27	06-Jun-27	-37	0%	0%	$11,292,592.97	$0.00	$0.00	
A2310	Not Starte	Saving Works	49	01-Apr-27	18-Apr-27	18-May-27	06-Jun-27	-37	0%	0%	$11,292,592.97	$0.00	$0.00	
Pounds			68	01-Apr-27	18-Apr-27	18-May-27	25-Jun-27	-37	0%	0%	$52,009,357.13	$0.00	$0.00	
A2320	Not Starte	Saving Works	68	01-Apr-27	18-Apr-27	18-May-27	25-Jun-27	-37	0%	0%	$52,009,357.13	$0.00	$0.00	
Road Crossing			68	01-Apr-27	18-Apr-27	30-Apr-27	25-Jun-27	-37	0%	0%	$3,351,680.43	$0.00	$0.00	
A2330	Not Starte	Saving Works	68	01-Apr-27	18-Apr-27	30-Apr-27	25-Jun-27	-37	0%	0%	$3,351,680.43	$0.00	$0.00	

© Oracle Corporation

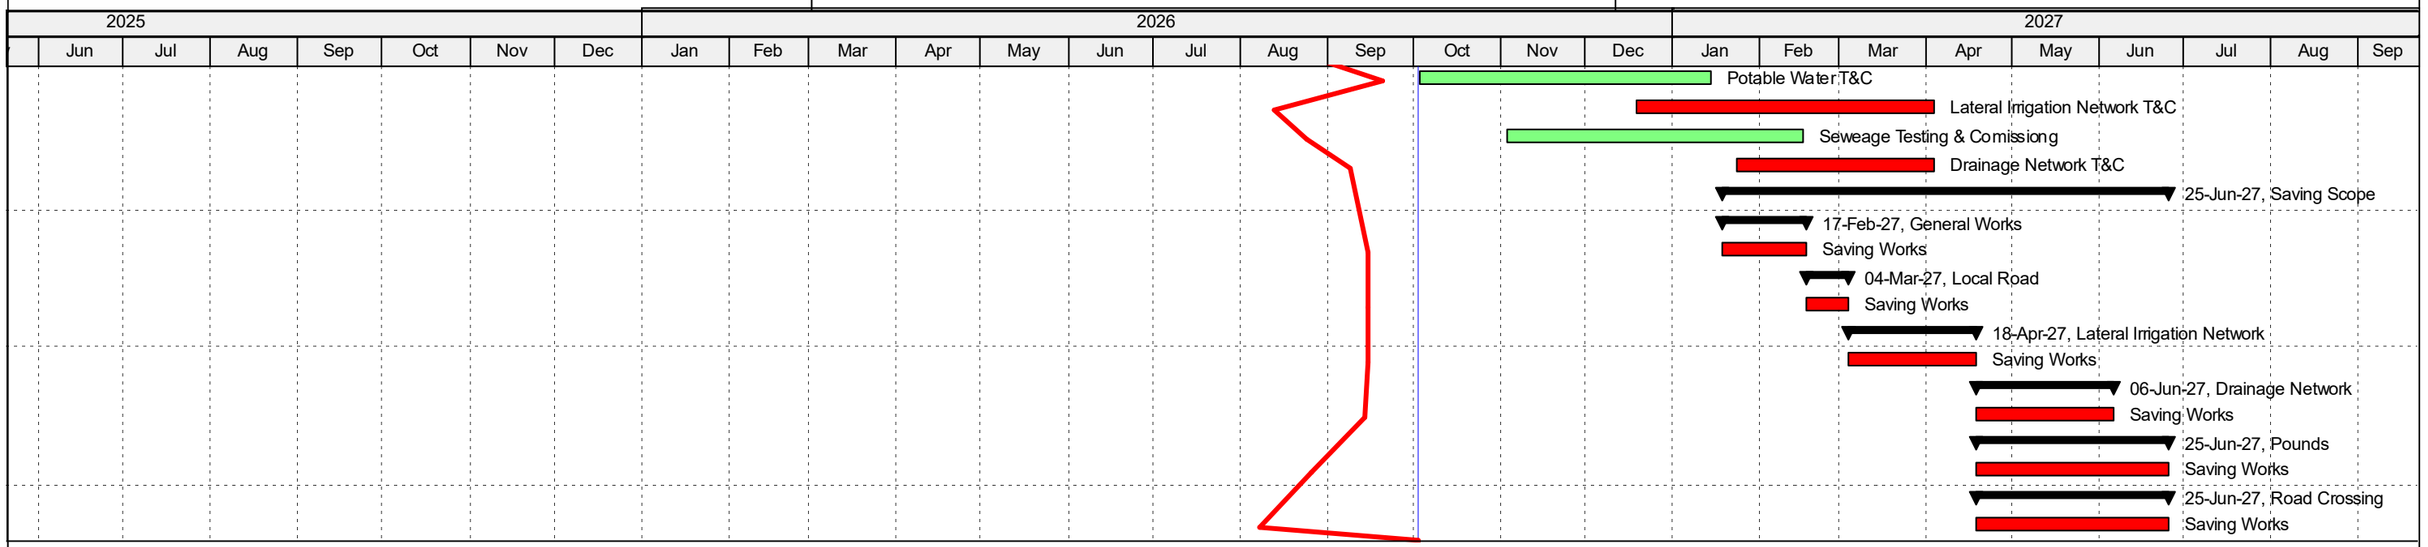

Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary

TASK filter: All Activities

© Oracle Corporation
