Infrastructure Development for Industrial City 1 in Jeddah

تطوير البنية التحتية بالمدينة الصناعية الأولى بجدة (1كم2)

CLIENT	CONTRACTOR	CONSULTANT	MODON PM	SITE HANDOVER	CONTRACT COMPLETION
MODON	Al Enjaz Company for Trading and Contracting	EGIS	Eng. Abdallah Aljulayfi	19-Nov-2025	18-Nov-2027

Scope: road works, storm, sewer, potable water and TSE networks, electrical works, fence and gates, a bridge and landscaping. Contract value 86.8M SAR, 24 months.

Status at a glance

Progress is measured as physical % complete, weighted by budgeted man-hours. At 73.4% against a plan of 48.0%, the project is 25.4% ahead (SPI 1.53). This week it gained 0.77% against 1.00% planned, so the lead narrowed slightly. Yet the schedule now forecasts completion 191 days after the contract date, one week later than last week.

PHYSICAL % COMPLETE

73.4% / 48.0% plan

▲ SPI 1.53 +25.4%

PROGRESS THIS WEEK

+0.77 % / +1.00% plan

▼ 0.23% below the weekly plan

CONTRACT TIME ELAPSED

46.9% · day 342 of 729

▼ Forecast finish 27-May-2028

INVOICED TO DATE (GROSS)

51.7% · 44.9M SAR

7 invoices in the log, last period ends 29-Sep-2026

Well ahead on progress, but the forecast finish is six months late.

Both the weekly report and the P6 update forecast completion on 27-May-2028, 191 days after the contract completion date of 18-Nov-2027, with −163 days of total float (−157 last week). Every open milestone slipped another 7 days this week. Roads and medium voltage, the WBS that is behind plan (73.5% against 100%, unchanged this week), depends on the MV network, which is waiting for the MODON–SEC agreement; MV cable, ring main units and lighting substations have not been ordered.

Site photos this week

Six photos from the Weekly Photos sheet of the 27-Oct-2026 weekly report, camera-stamped 25 and 26 Oct 2026 where the stamp is visible. Asphalt wearing course, telecom ducts, interlock paving and signboard foundations are in progress. Select a photo to view it larger, then use the arrows to move between photos.



Telecom pipes, local road L01

Duct pipes laid out along the trench. Stamped 26-Oct-2026, 10:07.



Asphalt wearing course

Tipper truck feeding the paver. No date stamp.



Telecom pipes in the trench, L01

Ducts placed in the trench. Stamped 26-Oct-2026, 06:25.




Interlock works

Crew laying paving blocks on the walkway. No date stamp.



Asphalt wearing course works

Roller on the new surface. Stamped 25-Oct-2026, 08:52.

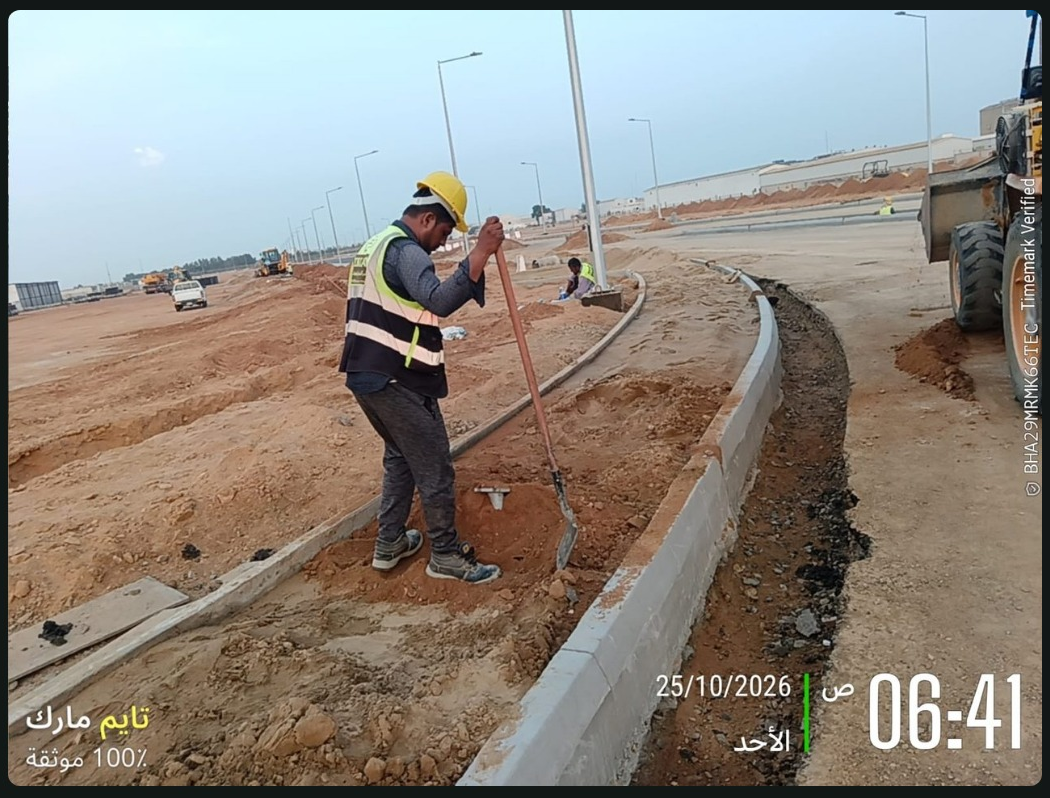


Signboard foundations

Excavation for a sign foundation beside the curb. Stamped 25-Oct-2026, 06:41.

Progress S-curve

Cumulative physical progress (man-hour weighted), monthly. Source: Physical-Chart Data sheet. The revised plan in the sheet is identical to the baseline, so only the baseline is drawn.

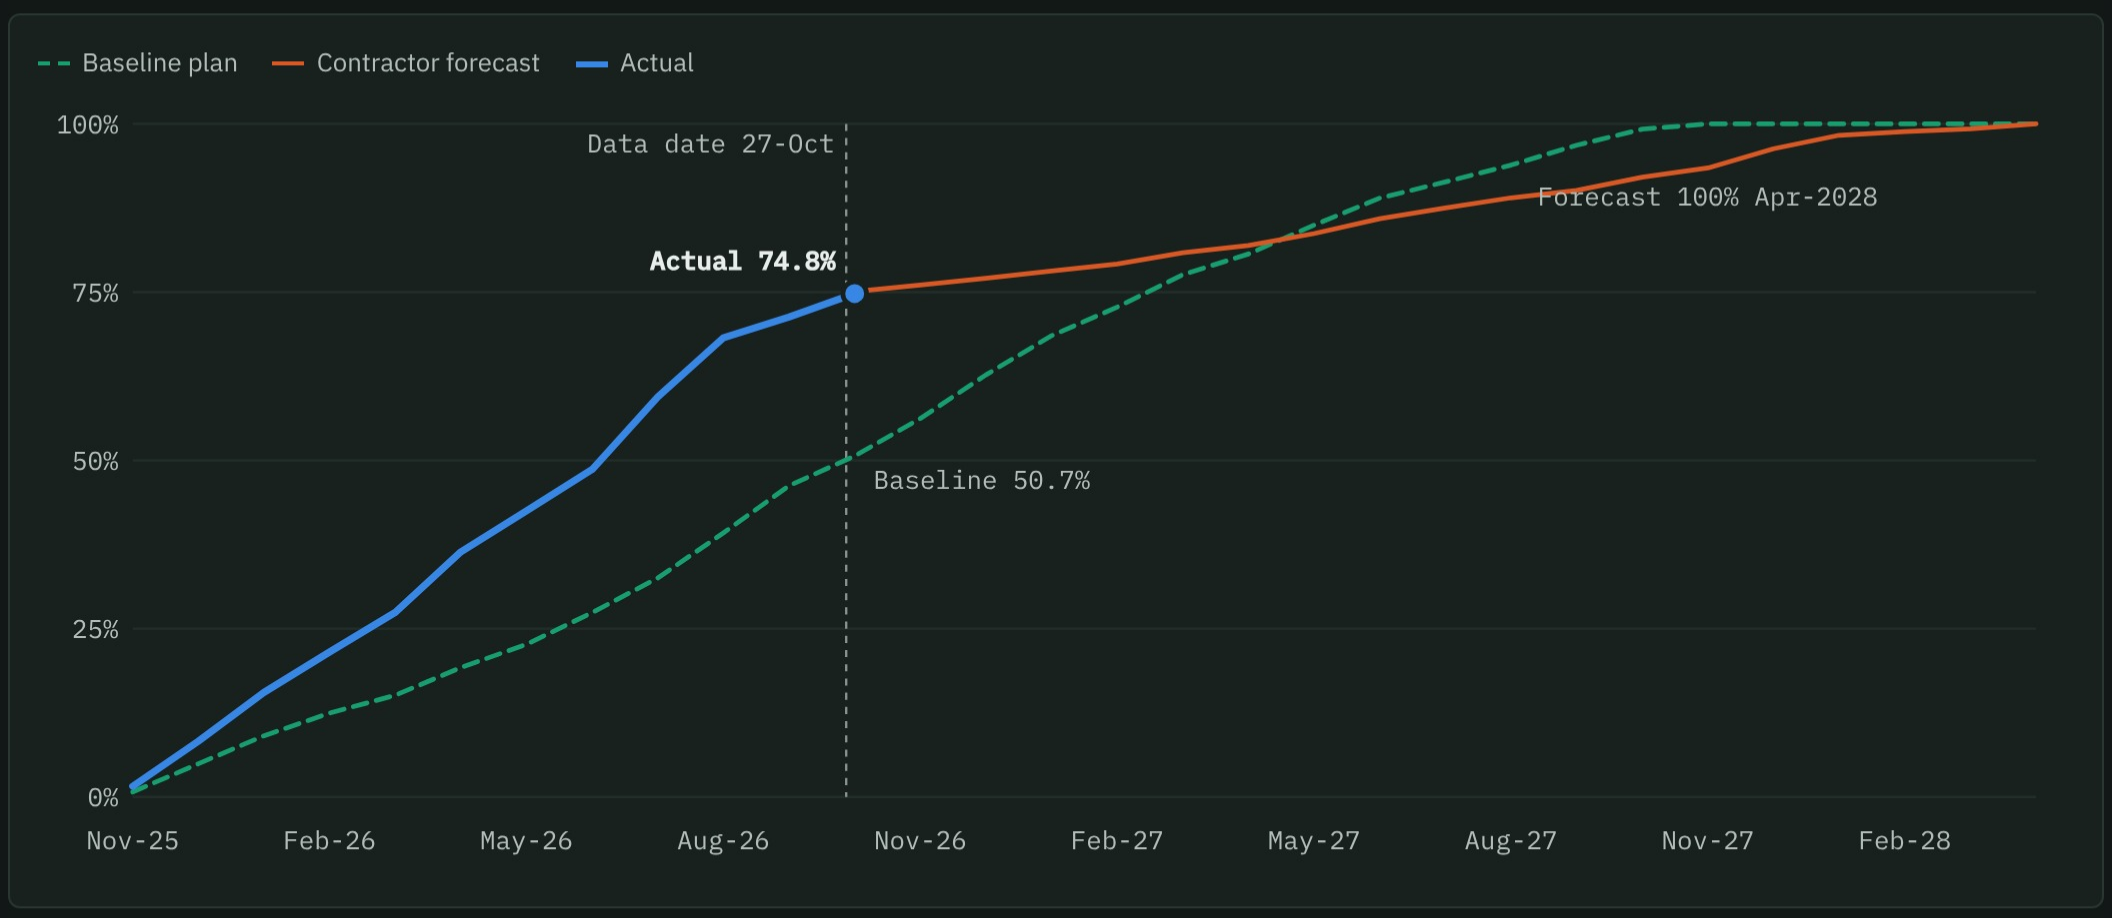

WEEK	PLANNED %	ACTUAL %	VARIANCE	GAINED THIS WEEK	SPI
Week before last	46.20	72.35	+26.14	–	1.57
20-Oct-2026	46.99	72.61	+25.63	+0.27	1.55
27-Oct-2026	**47.99**	**73.38**	**+25.40**	**+0.77**	**1.53**

Rows for 20 and 27 Oct come from the weekly reports of those dates; the first row is the "last week" column of the 20-Oct report, whose gain is not stated. The chart's October actual (74.8%) comes from the P6 export and is higher than the 73.4% on the report dashboard; see Data notes.

Progress by phase


Physical progress to date by WBS, weighted by budgeted man-hours. Construction sub-phases are listed under Construction.

PHASE	WEIGHT	PLANNED	ACTUAL	VARIANCE	SPI	STATUS
Mobilization	2.8%	100.0%	100.0%	0.0%	1.00	✓ Complete
Engineering	4.7%	100.0%	98.8%	−1.2%	0.99	▼ Slightly behind
Procurement	11.5%	43.5%	78.9%	+35.4%	1.81	▲ Ahead
Construction	76.3%	46.5%	72.6%	+26.1%	1.56	▲ Ahead
· Site demolition	1.0%	100.0%	100.0%	0.0%	1.00	✓ Complete
· Roads & medium voltage	14.0%	100.0%	73.5%	−26.5%	0.73	▼ Behind
· Deep infrastructure network	7.6%	100.0%	95.9%	−4.1%	0.96	▼ Slightly behind
· Shallow infrastructure network	27.8%	25.1%	78.2%	+53.2%	3.12	▲ Ahead
· Bridge	2.0%	56.3%	87.1%	+30.8%	1.55	▲ Ahead
· Outside boundary area (tie-in lines)	2.8%	52.0%	99.7%	+47.6%	1.92	▲ Ahead
· Roads finishing	9.2%	0.0%	75.9%	+75.9%	–	▲ Ahead
· Fence and gate	6.1%	55.0%	58.2%	+3.2%	1.06	▲ On track
· Roundabout & landscape	5.8%	0.0%	0.0%	0.0%	–	● Not yet due
Testing & commissioning	2.8%	0.0%	53.1%	+53.1%	–	▲ Ahead
Project close-out	1.9%	0.0%	0.0%	0.0%	–	● Not yet due
Total	100%	**48.0%**	**73.4%**	**+25.4%**	**1.53**	▲ Ahead

The schedule statistics for the P6 update (data date 27-Oct-2026) list 1,905 activities: 1,278 completed, 198 in progress and 419 not started. Of the 198 active activities, 93 are ahead and 105 behind. Critical-path activities fell from 457 to 448 and failed starts from 113 to 105.

Scope of work: quantities

Total, finished and remaining quantity for the major BOQ items, from the Major Quantities sheet of the 27-Oct-2026 weekly report. "This week" is the change from the 20-Oct-2026 report. The report gives no zone split and no backfilled quantity.

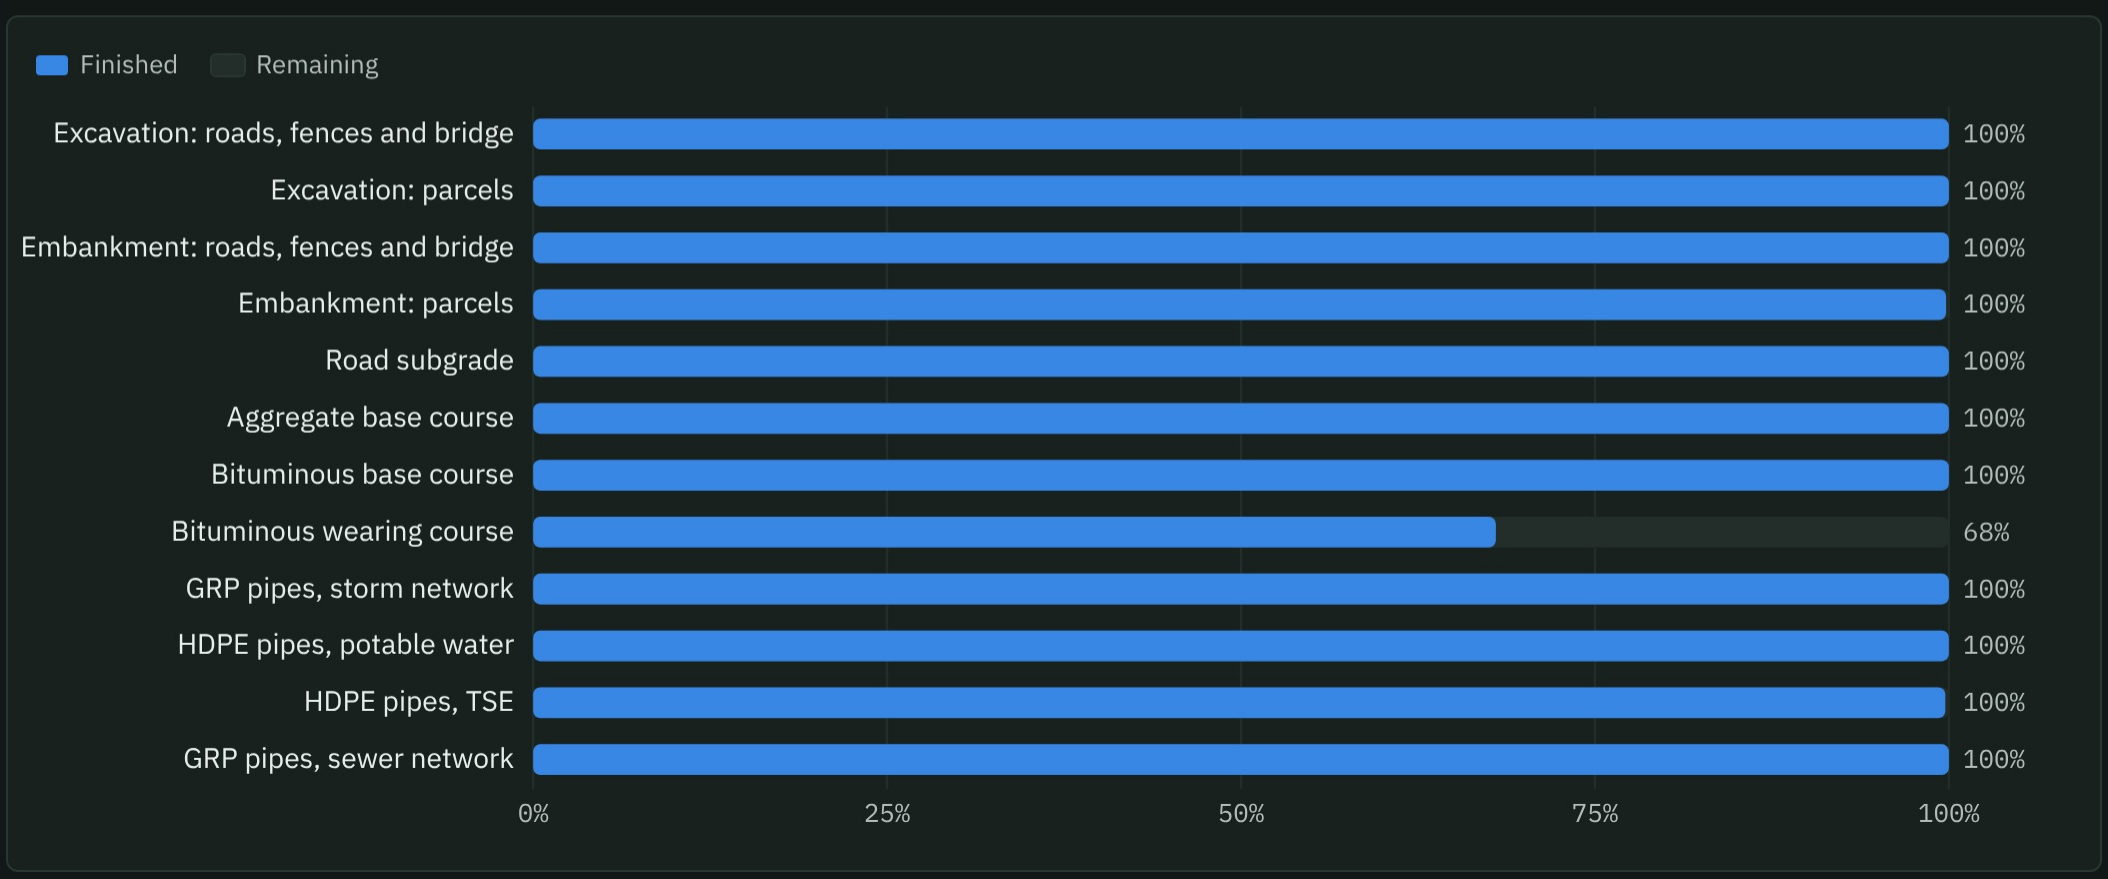

SCOPE ITEM	ZONE	UNIT	TOTAL	FINISHED	THIS WEEK	REMAINING	% FINISHED	BACKFILLED
Excavation: roads, fences and bridge	All	m³	116,177	116,177	0	0	100.0%	–
Excavation: parcels	All	m³	123,555	123,555	0	0	100.0%	–
Embankment: roads, fences and bridge	All	m³	80,920	80,920	0	0	100.0%	–
Embankment: parcels	All	m³	94,645	94,456	0	189.3	99.8%	–
Road subgrade	All	m³	34,694	34,694	0	0	100.0%	–
Aggregate base course	All	m³	23,129	23,129	0	0	100.0%	–
Bituminous base course	All	m³	8,290	8,290	0	0	100.0%	–
Bituminous wearing course	All	m³	5,920	4,026	+1,952	1,894	68.0%	–
GRP pipes, storm network	All	LM	5,650	5,650	0	0	100.0%	–
HDPE pipes, potable water	All	LM	12,075	12,075	0	0.3	100.0%	–
HDPE pipes, TSE	All	LM	8,722	8,700	0	22	99.7%	–
GRP pipes, sewer network	All	LM	6,244	6,244	0	0	100.0%	–

Asphalt wearing course is the only item that moved

1,951.6 m³ was laid this week, bringing it to 4,025.6 of 5,920 m³ (68.0%). All other earthworks, base course and pipe items are unchanged and complete or within 0.3% of their totals.

Milestones

Baseline dates and forecasts from the Milestones sheet of the weekly report, and forecasts and total float from the P6 export in the same workbook.

MILESTONE	BASELINE	WEEKLY REPORT FORECAST	P6 UPDATE FORECAST	P6 FLOAT (DAYS)	STATUS
Project start	19-Nov-2025	19-Nov-2025	19-Nov-2025 (actual)	–	✓ Done
Baseline time schedule	18-Dec-2025	18-Dec-2025	18-Dec-2025 (actual)	–	✓ Done
Finish mobilization	18-Dec-2025	04-Mar-2026	04-Mar-2026 (actual)	–	✓ Done late
Shop drawings, method statements and materials approved	19-Jan-2026	14-Nov-2026	14-Nov-2026	−61	▼ Late
All purchase orders issued	19-Jan-2026	08-Nov-2026	08-Nov-2026	−55	▼ Late
Roads & medium voltage complete	17-Sep-2026	25-Jan-2027	26-Jun-2027	−111	▼ Late
Deep infrastructure network complete	18-Nov-2026	26-Jun-2027	25-Jan-2027	39	? Conflicts with P6
Shallow infrastructure network complete	18-Mar-2027	10-Oct-2027	10-Oct-2027	−40	▼ Late
Completion of all works	18-Nov-2027	27-May-2028	27-May-2028	−163	▼ Late

The two sources swap the dates of two milestones.

The weekly report forecasts roads and medium voltage on 25-Jan-2027 and the deep network on 26-Jun-2027; the P6 export gives the same two dates the other way round. All other forecasts agree. Every open forecast moved 7 days later than in the 20-Oct report, so the approvals and purchase-order milestones (07-Nov and 01-Nov last week) are now due on 14-Nov and 08-Nov-2026.

Procurement of key materials

Share of the revised BOQ quantity delivered to site. Source: Material Monitoring sheet, weekly report 27-Oct-2026.



Medium-voltage materials: nothing ordered


MV cable (14,500 m), ring main units (4), street-lighting substations (4), kWh meters (4) and cable terminations (64) are not delivered. The Procurement Log shows the MV cable and substation orders on hold until the MODON–SEC electricity agreement is completed, with delivery now expected 30-Nov-2026.

Road finishing items

Asphalt wearing course 4,025.6 of 5,920 m³ delivered (68%, up from 35%). Pavement markings (3,780 m²) and paint on cement plaster (4,062 m²) not yet delivered. Overall, 108 of 113 purchase orders are issued and 105 of 113 materials are on site.

Manpower

Monthly manual (direct) head count on site, planned vs actual. Source: Manpower sheet.

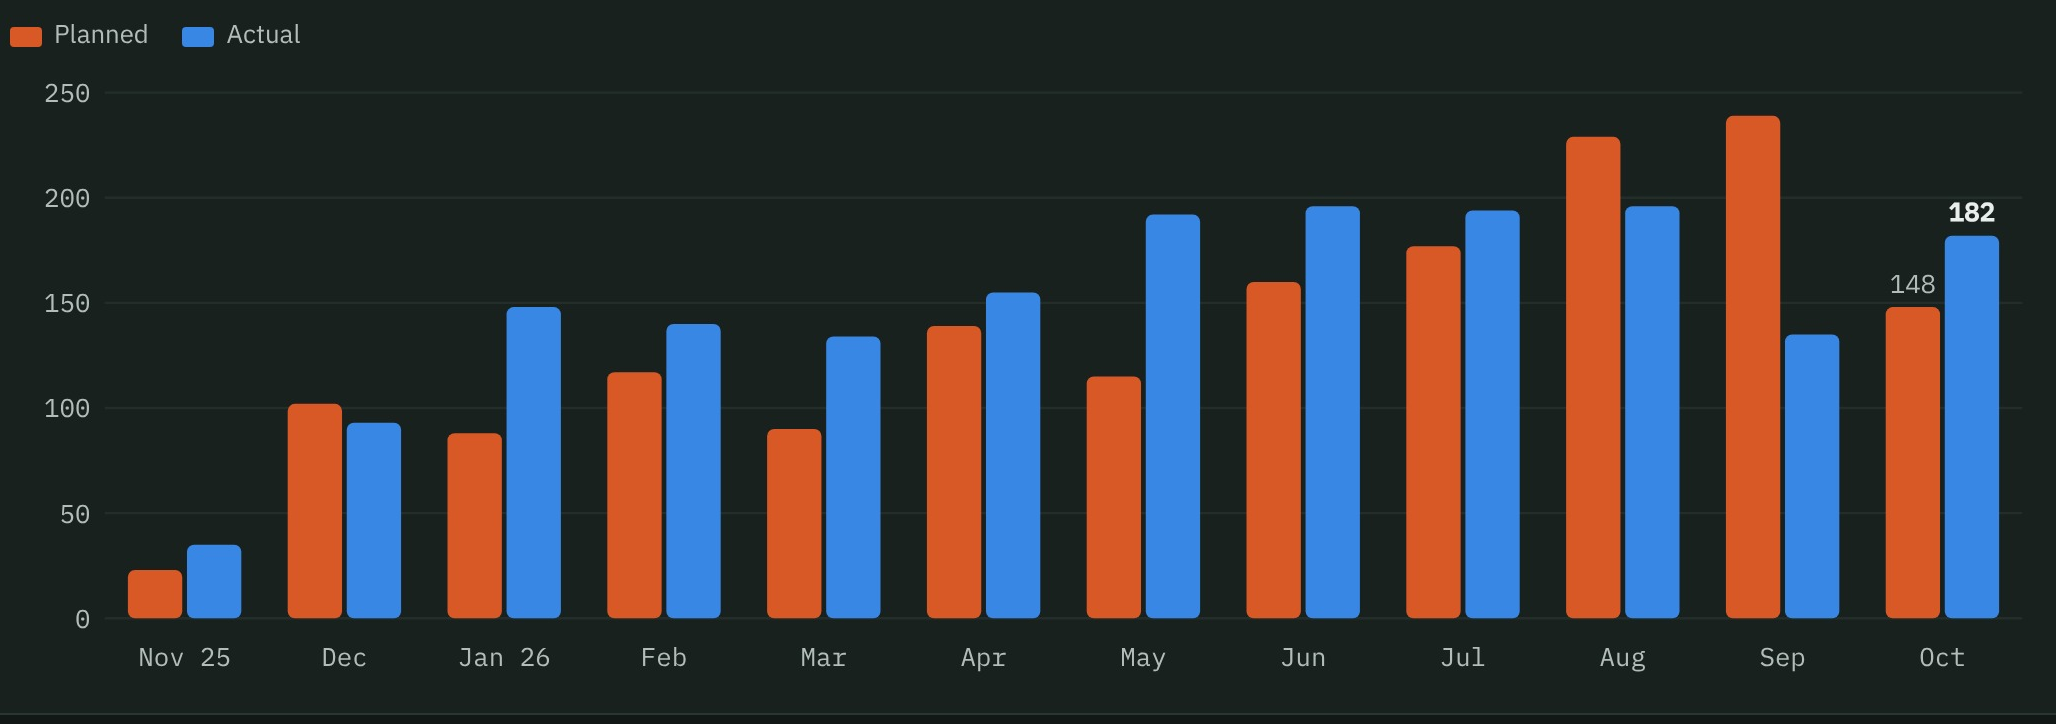

The 27-Oct report raises the October manual head count to 182 against 148 planned (+23%; the 20-Oct report gave 130). Non-manual staff are 48 against 22 planned. Equipment on site is 75 against 60 planned. The plan rises to 187 manual workers in November.

Cost and invoicing

Contract value

Original contract value	86,782,345
Revised contract value	86,782,345
Estimate at completion	86,782,345
Change orders	0

All values in SAR. No change orders are registered (CCO sheet).

Invoices

Invoices in the log	7
Gross value	44,851,849
Approved by PM (7, incl. VAT)	51,579,627
Paid (6, incl. VAT)	48,055,958
Retention / deductions	0 / 0
Advance payment	0

Gross invoicing is 51.7% of the contract value against 72.6% physical progress. Invoice 7 (period to 29-Sep-2026, 3,523,669 incl. VAT) is approved by the PM and was sent to accounts on 06-Oct-2026; it is not yet paid.

Health, safety and quality

Safety Score 0.73

Safe man-hours (cumulative)	474,226
Man-hours this week	9,216
Lost-time injuries	0
Fatalities	0
First-aid cases	0
Near misses	0
Inductions / toolbox talks (cumulative)	64 / 90

MODON HSE inspection 27-Oct-2026: 7 topics good, 13 need improvement and 3 failed (site waste management, HSE communications and meetings, project leadership site tours).

Quality Score 0.85

Field inspection requests issued / closed	5,541 / 5,461
FIRs with the consultant	59
Material inspections issued / closed	105 / 105
NCRs issued / closed	17 / 16
Site instructions issued / closed	21 / 21
Shop drawings pending	3

Consultant quality score 0.85 this week; average 0.83 across all audits.

Open issues and risks

ISSUE	OWNER	DETAIL
MODON–SEC agreement for medium voltage	Owner	Open since 15-Dec-2025, target closure 30-Dec-2025. MODON is following up with SEC for the electricity source; the contractor is waiting for a reply to letter 2818 of 13-Jan-2026.
MV materials on hold	Owner / Contractor	Orders for MV cable, ring main units and street-lighting substations wait for the agreement. The ring main unit order is marked "PO in delay"; it was required on site by 20-Oct-2026 and is still not ordered.
Completion forecast	Contractor	The schedule forecasts completion on 27-May-2028 with −163 days of float, 191 days after the contract date, although physical progress is 25.4% ahead of plan. The forecast has moved 7 days later in each of the last two reports.

The other two issues in the log are closed: tie-in permits from SEC, STC and NWC (closed 10-Feb-2026) and supplier prequalification for post-tensioning, bearings and expansion joints.

Data notes

Built from the 27-Oct-2026 weekly upload (W04), with the 20-Oct-2026 upload (W03) for this week's changes.

- Week number: the report states week 48.86 (whole weeks since site handover: 48); the file reference is WPR-049.
- Physical progress differs between sheets: the dashboard shows 73.4% (524,368 of 714,561 man-hours), while the P6 export and the Physical-Chart Data sheet show 74.8% (534,438 man-hours).

- The weekly summary file (works executed this week) and the Look Ahead and Conclusion sheets label cost-based progress as "actual"; this report uses physical % complete (man-hours) only. The weekly summary file also gives project code JDH3-03-011, contract value 86,742,345 and an expected finish of 30-Nov-2026, as does the Look Ahead sheet; the dashboard and P6 forecast 27-May-2028.
- MODON PM: Eng. Abdallah Aljulayfi in the General Information sheet; م. رضا المنشاوي in the Look Ahead sheet and the weekly summary file.
- Milestones: P6 and the weekly report still swap the roads/MV and deep-network forecast dates, and the dashboard's "Original (Baseline)" column shows latest-plan dates.
- Asphalt wearing course: the Major Quantities sheet shows 4,025.6 m³ laid and the Material Monitoring sheet 4,025.6 m³ delivered, but its "installed" column still shows 2,074 m³. The installed quantity of the 6,115 m low-voltage cable line fell from 2,063 m to 230 m.
- Schedule statistics do not add up: 1,278 completed + 198 in progress + 419 not started = 1,895, not 1,905. The "last week" failed-start count is 107, although the 20-Oct report gave 113 for that week.
- The October manpower actual was revised from 130 to 182 between the two reports. The HSE sheet repeats 9,216 man-hours for this week, the same as last week.
- The Procurement Log is unchanged from the 20-Oct upload (identical file). The Progress Certificate and the 3-week look-ahead PDF were not included in this upload.
- Invoices: the summary says 6 submitted invoices, but the log lists 7 and the 44,851,849 total includes the seventh. Approved and paid amounts include 15% VAT, while the submitted total is gross.
- HDPE pipes: the Major Quantities sheet does not name the network; potable water and TSE are inferred from quantities, and installed quantities differ from the Material Monitoring sheet.
- Equipment cumulative actual stays at 564 from July although monthly counts continue. Several dashboard cells show #REF! errors.

Compiled 01-Nov-2026 from the weekly report for the week ending 27-Oct-2026 (W04), with the 20-Oct-2026 report (W03) for this week's changes.
