
Development of the Technology City in Dammam -Upda
03-11-2026
3Week Lookahead Schedule

Activity ID	Activity Name	Original Duration	Start	Finish	BL Project Start	BL Project Finish	Budgeted Total Cost
Development of the Technology City in Dammam -Update 03-11-2026		217	22-Jul-26 A	13-Mar-27	23-Jun-26	28-Jan-27	19,522,189.79
Procurement Cycle		193	22-Jul-26 A	04-Mar-27	23-Jun-26	28-Jan-27	0.00
Short Lead Time Items		193	22-Jul-26 A	04-Mar-27	23-Jun-26	28-Jan-27	0.00
Infrastructure Networks		193	22-Jul-26 A	04-Mar-27	23-Jun-26	28-Jan-27	0.00
Road Works		1	02-Aug-26 A	03-Nov-26	02-Nov-26	05-Dec-26	0.00
Material Delivery & Site Inspection		1	02-Aug-26 A	03-Nov-26	02-Nov-26	05-Dec-26	0.00
Pre-Bituminous Construction		1	02-Aug-26 A	03-Nov-26	02-Nov-26	12-Nov-26	0.00
PRO-R25-RD-DL-	Material Delivery & Site Inspection for Subgrade of Road Works	0	02-Aug-26 A	03-Nov-26	02-Nov-26	02-Nov-26	0.00
PRO-R25-RD-DL-	Material Delivery & Site Inspection for Aggregate Base Course of Road Works	0	03-Nov-26	03-Nov-26	12-Nov-26	12-Nov-26	0.00
Bituminous Construction		0	03-Nov-26	03-Nov-26	05-Dec-26	05-Dec-26	0.00
PRO-R25-RD-DL-	Material Delivery & Site Inspection for Prime Coat of Road Works	0	03-Nov-26	03-Nov-26	05-Dec-26	05-Dec-26	0.00
PRO-R25-RD-DL-	Material Delivery & Site Inspection for Bituminous Base & Wearing Courses of Road	0	03-Nov-26	03-Nov-26	05-Dec-26	05-Dec-26	0.00
Pavement Works		0	03-Nov-26	03-Nov-26	12-Nov-26	12-Nov-26	0.00
PRO-R25-RD-DL-	Material Delivery & Site Inspection of Interlock Tiles for Landscaping	0	03-Nov-26	03-Nov-26	12-Nov-26	12-Nov-26	0.00
PRO-R25-RD-DL-	Material Delivery & Site Inspection of Curbstones for Landscaping	0	03-Nov-26	03-Nov-26	12-Nov-26	12-Nov-26	0.00
Traffic Signs Boards and Roads Marking		0	03-Nov-26	03-Nov-26	08-Nov-26	25-Nov-26	0.00
PRO-R25-RD-DL-	Material Delivery & Site Inspection of Traffic Signs Boards For Road Works	0	03-Nov-26	03-Nov-26	08-Nov-26	08-Nov-26	0.00
PRO-R25-RD-DL-	Material Delivery & Site Inspection of Road Markings For Road Works	0	03-Nov-26	03-Nov-26	25-Nov-26	25-Nov-26	0.00
Softscape and Planting Works		83	03-Nov-26	07-Feb-27	11-Jul-26	17-Oct-26	0.00
Issuance of Purchase Orders		6	03-Nov-26	09-Nov-26	11-Jul-26	19-Jul-26	0.00
Main Line Pipes		6	03-Nov-26	09-Nov-26	11-Jul-26	19-Jul-26	0.00
PRO-IR-PO-140	Issuance of Purchase Order for Softscape and Planting Works	6	03-Nov-26	09-Nov-26	12-Jul-26	19-Jul-26	0.00
PRO-IR-PO-150	Issuance of Purchase Order for Site Furnishings (Seating Bench,Stone Boulders and	6	03-Nov-26	09-Nov-26	11-Jul-26	18-Jul-26	0.00
Manufacturing of Material		90	10-Nov-26	07-Feb-27	18-Jul-26	17-Oct-26	0.00
Main Line Pipes		90	10-Nov-26	07-Feb-27	18-Jul-26	17-Oct-26	0.00
PRO-IR-MF-140	Manufacturing of Softscape and Planting Works	90	10-Nov-26	07-Feb-27	19-Jul-26	17-Oct-26	0.00
PRO-IR-MF-150	Manufacturing of Valves for Site Furnishings (Seating Bench,Stone Boulders and Gra	90	10-Nov-26	07-Feb-27	18-Jul-26	16-Oct-26	0.00
Sewage Network		124	13-Sep-26 A	02-Dec-26	15-Jul-26	21-Nov-26	0.00
Manufacturing of Material		130	28-Oct-26 A	02-Dec-26	15-Jul-26	21-Nov-26	0.00
Testing and Finishes		130	28-Oct-26 A	02-Dec-26	15-Jul-26	21-Nov-26	0.00
PRO-SW-MF-120	Manufacturing of Manhole Covers for Sewage Network	130	28-Oct-26 A	02-Dec-26	15-Jul-26	21-Nov-26	0.00
Material Delivery & Site Inspection		0	13-Sep-26 A	03-Nov-26	09-Aug-26	09-Aug-26	0.00
Main Line Sections		0	13-Sep-26 A	03-Nov-26	09-Aug-26	09-Aug-26	0.00
PRO-R25-SW-DL-	Material Delivery & Site Inspection of Manholes for Sewage Network	0	13-Sep-26 A	03-Nov-26	09-Aug-26	09-Aug-26	0.00
Storm Drainage Network		169	02-Aug-26 A	10-Feb-27	15-Jul-26	22-Oct-26	0.00
Manufacturing of Material		100	03-Nov-26	10-Feb-27	15-Jul-26	22-Oct-26	0.00
Testing and Finishes		100	03-Nov-26	10-Feb-27	15-Jul-26	22-Oct-26	0.00
PRO-SD-MF-120	Manufacturing of Materials for Manhole Covers of Storm Drainage Network	100	03-Nov-26	10-Feb-27	15-Jul-26	22-Oct-26	0.00
PRO-SD-MF-140	Manufacturing of Materials for Catch Basin Covers of Storm Drainage Network	100	03-Nov-26	10-Feb-27	15-Jul-26	22-Oct-26	0.00
Material Delivery & Site Inspection		11	02-Aug-26 A	03-Nov-26	27-Jul-26	09-Aug-26	0.00
Main Line Sections		0	02-Aug-26 A	03-Nov-26	09-Aug-26	09-Aug-26	0.00
PRO-R25-SD-DL-	Material Delivery & Site Inspection of Manholes of Storm Drainage Network	0	02-Aug-26 A	03-Nov-26	09-Aug-26	09-Aug-26	0.00
Catch Basin Sections		0	02-Aug-26 A	03-Nov-26	27-Jul-26	27-Jul-26	0.00
PRO-R25-SD-DL-	Material Delivery & Site Inspection of Catch Basins for Storm Drainage Network	0	02-Aug-26 A	03-Nov-26	27-Jul-26	27-Jul-26	0.00
PRO-R25-SD-DL-	Material Delivery & Site Inspection of Catch Basin Pipes for Storm Drainage Network	0	02-Aug-26 A	03-Nov-26	27-Jul-26	27-Jul-26	0.00
Potable Water Network		130	30-Jul-26 A	04-Mar-27	07-Jul-26	06-Nov-26	0.00
Issuance of Purchase Orders		10	03-Nov-26	14-Nov-26	08-Jul-26	19-Jul-26	0.00
Testing and Finishes		10	03-Nov-26	14-Nov-26	08-Jul-26	19-Jul-26	0.00
PRO-PW-PO-130	Issuance of Purchase Order for Surface Box of Potable Water Network	10	03-Nov-26	14-Nov-26	08-Jul-26	19-Jul-26	0.00
Manufacturing of Material		110	15-Nov-26	04-Mar-27	20-Jul-26	06-Nov-26	0.00
Testing and Finishes		110	15-Nov-26	04-Mar-27	20-Jul-26	06-Nov-26	0.00
PRO-PW-MF-130	Manufacturing for Surface Box of Potable Water Network	110	15-Nov-26	04-Mar-27	20-Jul-26	06-Nov-26	0.00
1st Material Delivery & Site Inspection		71	30-Jul-26 A	03-Nov-26	07-Jul-26	28-Sep-26	0.00

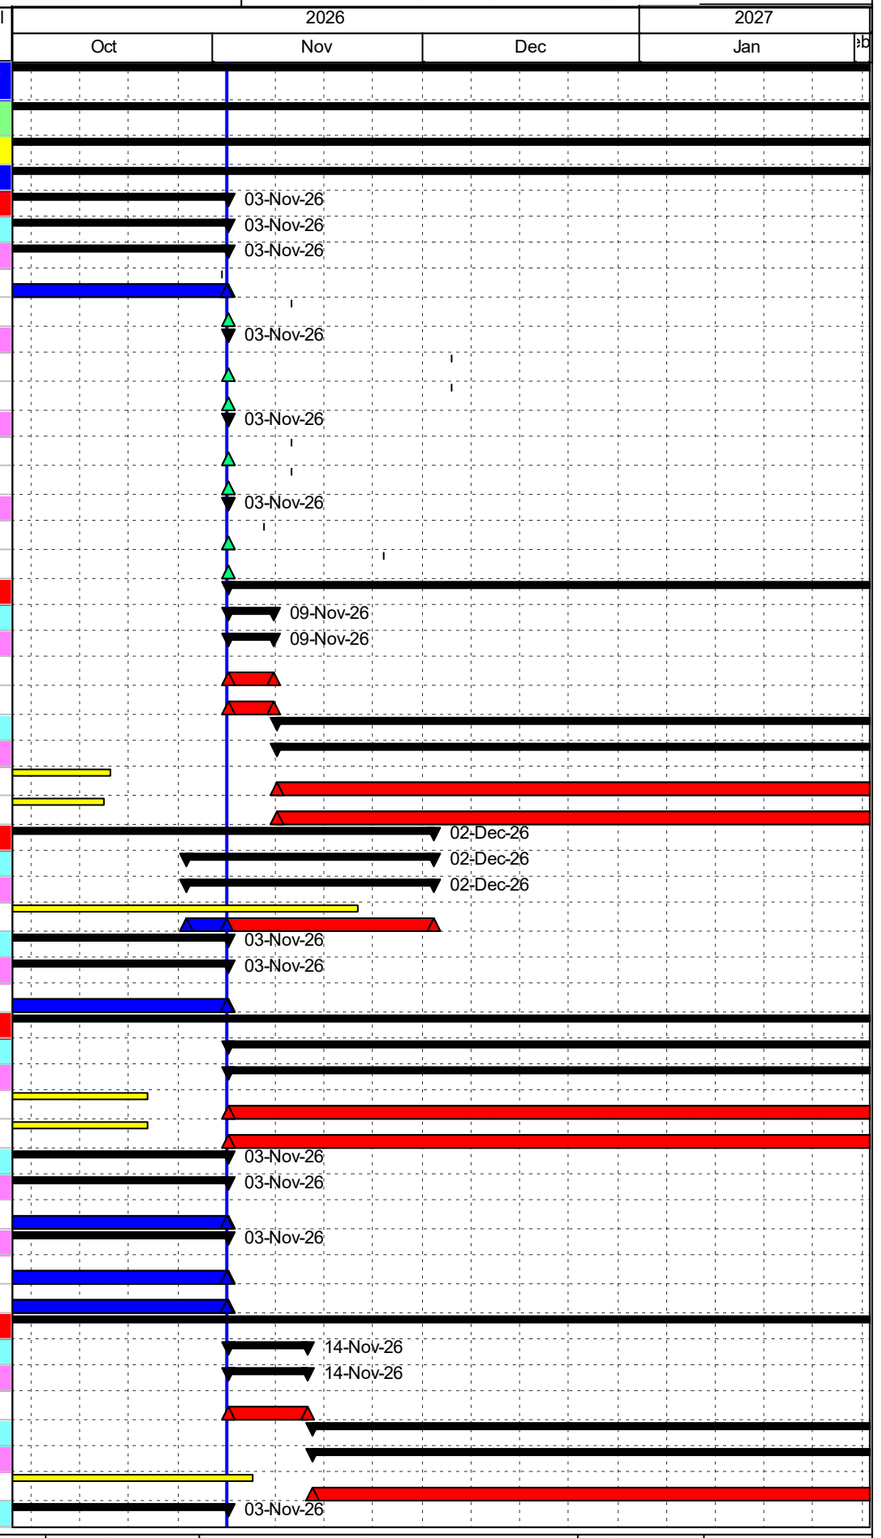


Primary Baseline
Remaining Work
Critical Remaining Work
Actual Work
Baseline Milestone
Milestone
Summary

Date	Revision	Checked	Approved
03-Nov-26	Third Industrial City		

Development of the Technology City in Dammam -Upda
03-11-2026
3Week Lookahead Schedule

Activity ID	Activity Name	Original Duration	Start	Finish	BL Project Start	BL Project Finish	Budgeted Total Cost
Main Line Sections		71	30-Jul-26 A	03-Nov-26	07-Jul-26	28-Sep-26	0.00
PRO-PW-1DL-100	1ST Material Delivery for Main Line Pipes of Potable Water Network(Remaining)	71	30-Jul-26 A	03-Nov-26	07-Jul-26	28-Sep-26	0.00
Material Delivery & Site Inspection		119	02-Aug-26 A	17-Jan-27	27-Sep-26	20-Oct-26	0.00
Main Line Sections		119	02-Aug-26 A	17-Jan-27	29-Sep-26	20-Oct-26	0.00
PRO-R25-PW-DL-	Material Delivery & Site Inspection of Main Line Pipes for Potable Water Network(Re	0	02-Aug-26 A	17-Jan-27	29-Sep-26	29-Sep-26	0.00
PRO-R25-PW-DL-	Material Delivery & Site Inspection of Valves for Potable Water Network	0	31-Oct-26 A	03-Nov-26	20-Oct-26	20-Oct-26	0.00
Fire Hydrant		0	31-Oct-26 A	03-Nov-26	27-Sep-26	27-Sep-26	0.00
PRO-R25-PW-DL-	Material Delivery & Site Inspection of Fire Hydrants for Potable Water Network	0	31-Oct-26 A	03-Nov-26	27-Sep-26	27-Sep-26	0.00
Irrigation Network		170	22-Jul-26 A	07-Feb-27	15-Jul-26	19-Oct-26	0.00
Issuance of Purchase Orders		6	03-Nov-26	09-Nov-26	15-Jul-26	21-Jul-26	0.00
Main Line Pipes		6	03-Nov-26	09-Nov-26	15-Jul-26	21-Jul-26	0.00
PRO-IR-PO-110	Issuance of Purchase Order for Valves of Irrigation Network	6	03-Nov-26	09-Nov-26	15-Jul-26	21-Jul-26	0.00
Manufacturing of Material		90	10-Nov-26	07-Feb-27	22-Jul-26	19-Oct-26	0.00
Main Line Pipes		90	10-Nov-26	07-Feb-27	22-Jul-26	19-Oct-26	0.00
PRO-IR-MF-110	Manufacturing of Valves for Irrigation Network	90	10-Nov-26	07-Feb-27	22-Jul-26	19-Oct-26	0.00
1st Material Delivery & Site Inspection		5	22-Jul-26 A	07-Nov-26	05-Oct-26	11-Oct-26	0.00
Main Line Pipes		5	22-Jul-26 A	07-Nov-26	05-Oct-26	11-Oct-26	0.00
PRO-IR-1DL-100	1ST Material Delivery for Main Line Pipes of Irrigation Network	5	22-Jul-26 A	07-Nov-26	05-Oct-26	11-Oct-26	0.00
Material Delivery & Site Inspection		0	07-Nov-26	07-Nov-26	11-Oct-26	11-Oct-26	0.00
Main Line Pipes		0	07-Nov-26	07-Nov-26	11-Oct-26	11-Oct-26	0.00
PRO-R25-IR-DL-1	Material Delivery & Site Inspection of Main Line Pipes for Irrigation Network	0	07-Nov-26	07-Nov-26	11-Oct-26	11-Oct-26	0.00
Treated Sewage Effluent (Tse)		104	02-Aug-26 A	07-Feb-27	27-Jun-26	10-Oct-26	0.00
Issuance of Purchase Orders		6	03-Nov-26	09-Nov-26	27-Jun-26	04-Jul-26	0.00
Main Line Pipes		6	03-Nov-26	09-Nov-26	27-Jun-26	04-Jul-26	0.00
PRO-TSE-PO-130	Issuance of Purchase Order for Valves of Treated Sewage Effluent (Tse)	6	03-Nov-26	09-Nov-26	27-Jun-26	04-Jul-26	0.00
Manufacturing of Material		90	10-Nov-26	07-Feb-27	04-Jul-26	02-Oct-26	0.00
Main Line Pipes		90	10-Nov-26	07-Feb-27	04-Jul-26	02-Oct-26	0.00
PRO-TSE-MF-130	Manufacturing of Valves for Treated Sewage Effluent (Tse)	90	10-Nov-26	07-Feb-27	04-Jul-26	02-Oct-26	0.00
Material Delivery & Site Inspection		0	02-Aug-26 A	03-Nov-26	10-Oct-26	10-Oct-26	0.00
Main Line Pipes		0	02-Aug-26 A	03-Nov-26	10-Oct-26	10-Oct-26	0.00
PRO-R25-TSE-DL-	Material Delivery & Site Inspection of Main Line Pipes for Treated Sewage Effluent (T	0	02-Aug-26 A	03-Nov-26	10-Oct-26	10-Oct-26	0.00
Medium Voltage Network		88	03-Nov-26	14-Feb-27	23-Jun-26	19-Oct-26	0.00
Issuance of Purchase Orders		12	03-Nov-26	16-Nov-26	23-Jun-26	21-Jul-26	0.00
Cabling Works		12	03-Nov-26	16-Nov-26	23-Jun-26	06-Jul-26	0.00
PRO-MV-PO-100	Issuance of Purchase Order for Medium Voltage Cables of Medium Voltage Network	12	03-Nov-26	16-Nov-26	23-Jun-26	06-Jul-26	0.00
Termination and Testing Works		12	03-Nov-26	16-Nov-26	08-Jul-26	21-Jul-26	0.00
PRO-MV-PO-120	Issuance of Purchase Order for Termination and Joints Kits of Medium Voltage Netw	12	03-Nov-26	16-Nov-26	08-Jul-26	21-Jul-26	0.00
Manufacturing of Material		90	17-Nov-26	14-Feb-27	07-Jul-26	19-Oct-26	0.00
Cabling Works		60	17-Nov-26	15-Jan-27	07-Jul-26	04-Sep-26	0.00
PRO-MV-MF-100	Manufacturing of Medium Voltage Cables for Medium Voltage Network	60	17-Nov-26	15-Jan-27	07-Jul-26	04-Sep-26	0.00
Termination and Testing Works		90	17-Nov-26	14-Feb-27	22-Jul-26	19-Oct-26	0.00
PRO-MV-MF-110	Manufacturing of Termination and Joints Kits for Medium Voltage Network	90	17-Nov-26	14-Feb-27	22-Jul-26	19-Oct-26	0.00
Low Voltage and Street Lighting Network		41	03-Nov-26	20-Dec-26	28-Sep-26	28-Jan-27	0.00
1st Material Delivery & Site Inspection		15	03-Nov-26	19-Nov-26	28-Sep-26	29-Dec-26	0.00
Cabling Works		6	03-Nov-26	09-Nov-26	28-Sep-26	04-Oct-26	0.00
PRO-SL-1DL-100	1ST Material Delivery for Lighting Cables of Street Lighting Network	6	03-Nov-26	09-Nov-26	28-Sep-26	04-Oct-26	0.00
Lighting Poles Works		6	03-Nov-26	09-Nov-26	28-Sep-26	19-Dec-26	0.00
PRO-SL-1DL-110	1ST Material Delivery for Lighting Poles Foundations of Street Lighting Network	6	03-Nov-26	09-Nov-26	28-Sep-26	04-Oct-26	0.00
PRO-SL-1DL-120	1ST Material Delivery for Lighting Poles of Street Lighting Network	6	03-Nov-26	09-Nov-26	28-Sep-26	04-Oct-26	0.00
PRO-SL-1DL-140	1ST Material Delivery for Lighting Fixtures of Street Lighting Network	6	03-Nov-26	09-Nov-26	13-Dec-26	19-Dec-26	0.00
Distribution Panel Board		6	03-Nov-26	09-Nov-26	24-Oct-26	29-Oct-26	0.00
PRO-SL-1DL-160	1ST Material Delivery for Distrubution Panel Boards of Street Lighting Network	6	03-Nov-26	09-Nov-26	24-Oct-26	29-Oct-26	0.00
Termination and Testing Works		15	03-Nov-26	19-Nov-26	03-Nov-26	29-Dec-26	0.00
PRO-SL-1DL-130	1ST Material Delivery for Fuse Boxes of Street Lighting Network	15	03-Nov-26	19-Nov-26	13-Dec-26	29-Dec-26	0.00

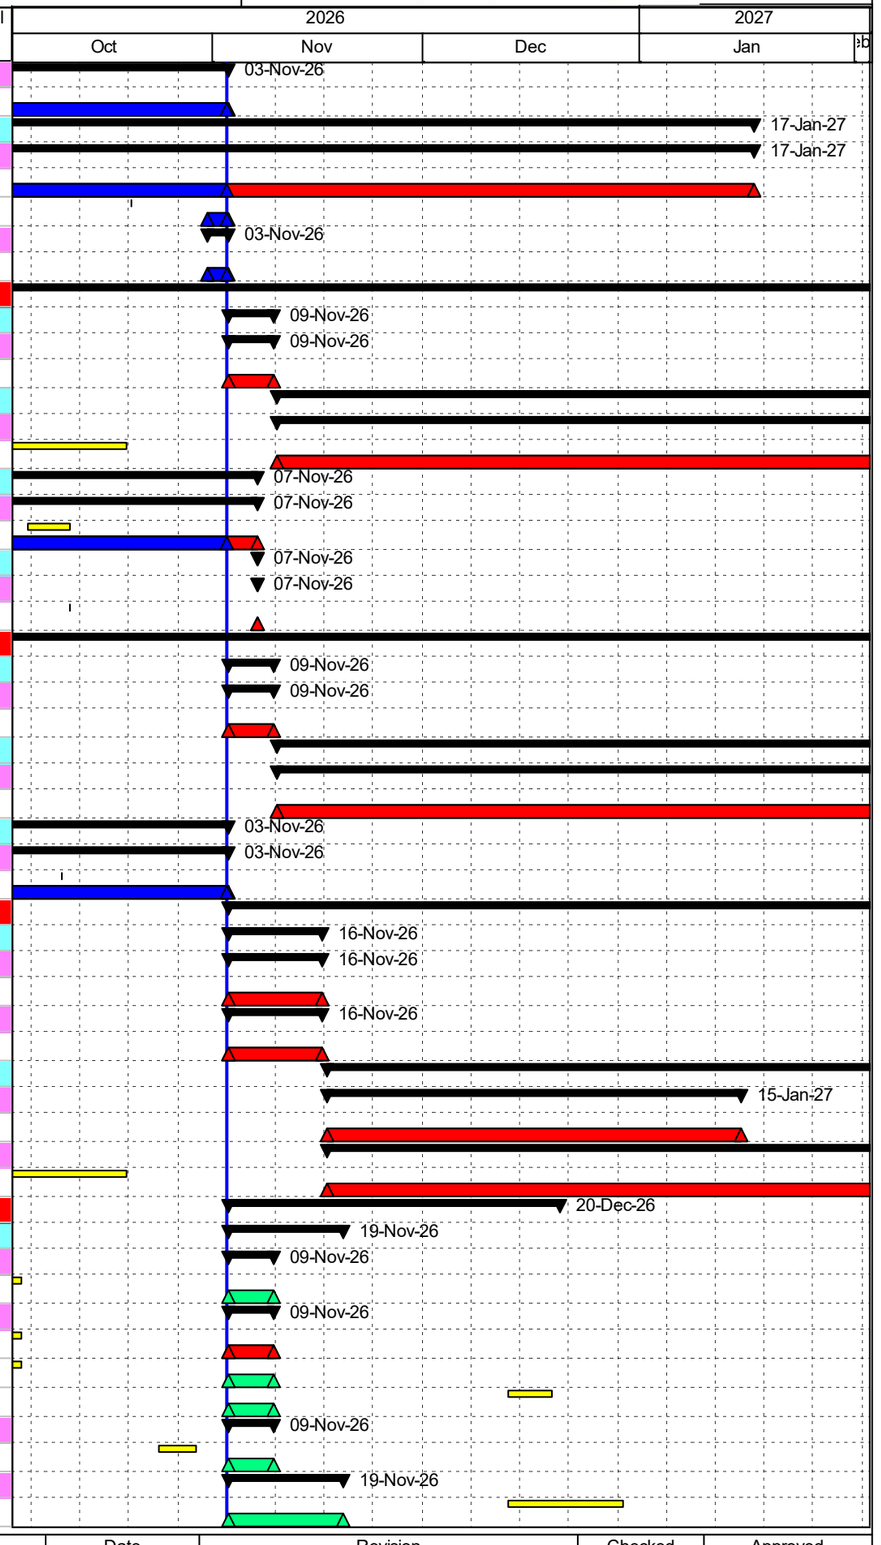


Primary Baseline | Actual Work | Summary
Remaining Work | Baseline Milestone
Critical Remaining Work | Milestone

Date	Revision	Checked	Approved
03-Nov-26	Third Industrial City		

Development of the Technology City in Dammam -Upda
03-11-2026
3Week Lookahead Schedule

Activity ID	Activity Name	Original Duration	Start	Finish	BL Project Start	BL Project Finish	Budgeted Total Cost
PRO-SL-1DL-170	1ST Material Delivery for Cable Lugs of Street Lighting Network	15	03-Nov-26	19-Nov-26	03-Nov-26	21-Nov-26	0.00
Earthing System Works		6	03-Nov-26	09-Nov-26	03-Dec-26	09-Dec-26	0.00
PRO-SL-1DL-150	1ST Material Delivery for Lighting Earthing of Street Lighting Network	6	03-Nov-26	09-Nov-26	03-Dec-26	09-Dec-26	0.00
Material Delivery & Site Inspection		35	10-Nov-26	20-Dec-26	05-Oct-26	28-Jan-27	0.00
Cabling Works		0	10-Nov-26	10-Nov-26	05-Oct-26	05-Oct-26	0.00
PRO-R25-SL-DL-1	Material Delivery & Site Inspection of Lighting Cables for Street Lighting Network	0	10-Nov-26	10-Nov-26	05-Oct-26	05-Oct-26	0.00
Lighting Poles Works		18	10-Nov-26	30-Nov-26	05-Oct-26	20-Dec-26	0.00
PRO-R25-SL-DL-1	Material Delivery & Site Inspection of Lighting Poles Foundations for Street Lighting I	18	10-Nov-26	30-Nov-26	05-Oct-26	25-Oct-26	0.00
PRO-R25-SL-DL-1	Material Delivery & Site Inspection of Lighting Poles for Street Lighting Network	0	10-Nov-26	10-Nov-26	05-Oct-26	05-Oct-26	0.00
PRO-R25-SL-DL-1	Material Delivery & Site Inspection of Lighting Fixtures for Street Lighting Network	0	10-Nov-26	10-Nov-26	20-Dec-26	20-Dec-26	0.00
Distribution Panel Board		0	10-Nov-26	10-Nov-26	31-Oct-26	31-Oct-26	0.00
PRO-R25-SL-DL-1	Material Delivery & Site Inspection of Distrubution Panel Boards for Street Lighting N	0	10-Nov-26	10-Nov-26	31-Oct-26	31-Oct-26	0.00
Termination and Testing Works		26	21-Nov-26	20-Dec-26	21-Nov-26	28-Jan-27	0.00
PRO-R25-SL-DL-1	Material Delivery & Site Inspection of Fuse Boxes for Street Lighting Network	26	21-Nov-26	20-Dec-26	30-Dec-26	28-Jan-27	0.00
PRO-R25-SL-DL-1	Material Delivery & Site Inspection of Cable Lugs for Street Lighting Network	26	21-Nov-26	20-Dec-26	21-Nov-26	21-Dec-26	0.00
Earthing System Works		0	10-Nov-26	10-Nov-26	10-Dec-26	10-Dec-26	0.00
PRO-R25-SL-DL-1	Material Delivery & Site Inspection of Lighting Earthing for Street Lighting Network	0	10-Nov-26	10-Nov-26	10-Dec-26	10-Dec-26	0.00
Telecom Network		83	03-Nov-26	07-Feb-27	07-Jul-26	11-Oct-26	0.00
Issuance of Purchase Orders		6	03-Nov-26	09-Nov-26	07-Jul-26	13-Jul-26	0.00
Ducts Works		6	03-Nov-26	09-Nov-26	07-Jul-26	13-Jul-26	0.00
PRO-TE-PO-100	Issuance of Purchase Order for Ducts forTelecom Network	6	03-Nov-26	09-Nov-26	07-Jul-26	13-Jul-26	0.00
Manholes Works		6	03-Nov-26	09-Nov-26	07-Jul-26	13-Jul-26	0.00
PRO-TE-PO-110	Issuance of Purchase Order for Manholes forTelecom Network	6	03-Nov-26	09-Nov-26	07-Jul-26	13-Jul-26	0.00
CCTV System Wroks		6	03-Nov-26	09-Nov-26	07-Jul-26	13-Jul-26	0.00
PRO-CTV-PO-100	Issuance of Purchase Order for Civil and Finishes Works of CCTV Complete System	6	03-Nov-26	09-Nov-26	07-Jul-26	13-Jul-26	0.00
Manufacturing of Material		90	10-Nov-26	07-Feb-27	14-Jul-26	11-Oct-26	0.00
Ducts Works		60	10-Nov-26	08-Jan-27	14-Jul-26	11-Sep-26	0.00
PRO-TE-MF-100	Manufacturing of Ducts for Telecom Network	60	10-Nov-26	08-Jan-27	14-Jul-26	11-Sep-26	0.00
Manholes Works		90	10-Nov-26	07-Feb-27	14-Jul-26	11-Oct-26	0.00
PRO-TE-MF-110	Manufacturing of Manholes for Telecom Network	90	10-Nov-26	07-Feb-27	14-Jul-26	11-Oct-26	0.00
CCTV System Wroks		90	10-Nov-26	07-Feb-27	14-Jul-26	11-Oct-26	0.00
PRO-CTV-MF-100	Manufacturing of Civil and Finishes Works for CCTV Complete System	90	10-Nov-26	07-Feb-27	14-Jul-26	11-Oct-26	0.00
Superstructure Works		77	21-Oct-26 A	31-Jan-27	13-Jul-26	11-Oct-26	0.00
Manufacturing of Material		90	03-Nov-26	31-Jan-27	13-Jul-26	11-Oct-26	0.00
Softscape and Planting Works		90	03-Nov-26	31-Jan-27	13-Jul-26	11-Oct-26	0.00
PRO-FE-CV-MF-70	Manufacturing of Civil Works for Softscape and Planting Works	90	03-Nov-26	31-Jan-27	13-Jul-26	11-Oct-26	0.00
1st Material Delivery & Site Inspection		1	21-Oct-26 A	03-Nov-26	23-Aug-26	23-Aug-26	0.00
Storage Tank (TSE)		1	21-Oct-26 A	03-Nov-26	23-Aug-26	23-Aug-26	0.00
PRO-TSE-CV-1DL-5	1ST Material Delivery for Civil Works for Civil Works for Storage Tank (TSE)	1	21-Oct-26 A	03-Nov-26	23-Aug-26	23-Aug-26	0.00
Material Delivery & Site Inspection		0	03-Nov-26	03-Nov-26	23-Aug-26	23-Aug-26	0.00
Storage Tank (TSE)		0	03-Nov-26	03-Nov-26	23-Aug-26	23-Aug-26	0.00
PRO-TSE-CV-DL-6(	Material Delivery & Site Inspection for Civil Works for Storage Tank (TSE)	0	03-Nov-26	03-Nov-26	23-Aug-26	23-Aug-26	0.00
Long Lead Time Items		71	26-Aug-26 A	01-Jan-27	23-Jun-26	05-Oct-26	0.00
Infrastructure Networks		20	03-Nov-26	25-Nov-26	23-Jun-26	15-Jul-26	0.00
CCTV System Wroks of Telecom Network		20	03-Nov-26	25-Nov-26	23-Jun-26	15-Jul-26	0.00
Issuance of Purchase Orders		20	03-Nov-26	25-Nov-26	23-Jun-26	15-Jul-26	0.00
PRO-CTV-LL-PO-1(	Issuance of Purchase Order for Low Current Works of CCTV Complete System with	20	03-Nov-26	25-Nov-26	23-Jun-26	15-Jul-26	0.00
Superstructure Works		71	26-Aug-26 A	01-Jan-27	04-Jul-26	05-Oct-26	0.00
Pump Stations		60	26-Aug-26 A	24-Nov-26	07-Aug-26	05-Oct-26	0.00
Manufacturing of Material		60	26-Aug-26 A	24-Nov-26	07-Aug-26	05-Oct-26	0.00
PRO-SPS-LL-MF-10	Manufacturing of Electromechanical Works for Pump Stations	60	26-Aug-26 A	24-Nov-26	07-Aug-26	05-Oct-26	0.00
Lift Stations		60	03-Nov-26	01-Jan-27	07-Aug-26	05-Oct-26	0.00
Manufacturing of Material		60	03-Nov-26	01-Jan-27	07-Aug-26	05-Oct-26	0.00

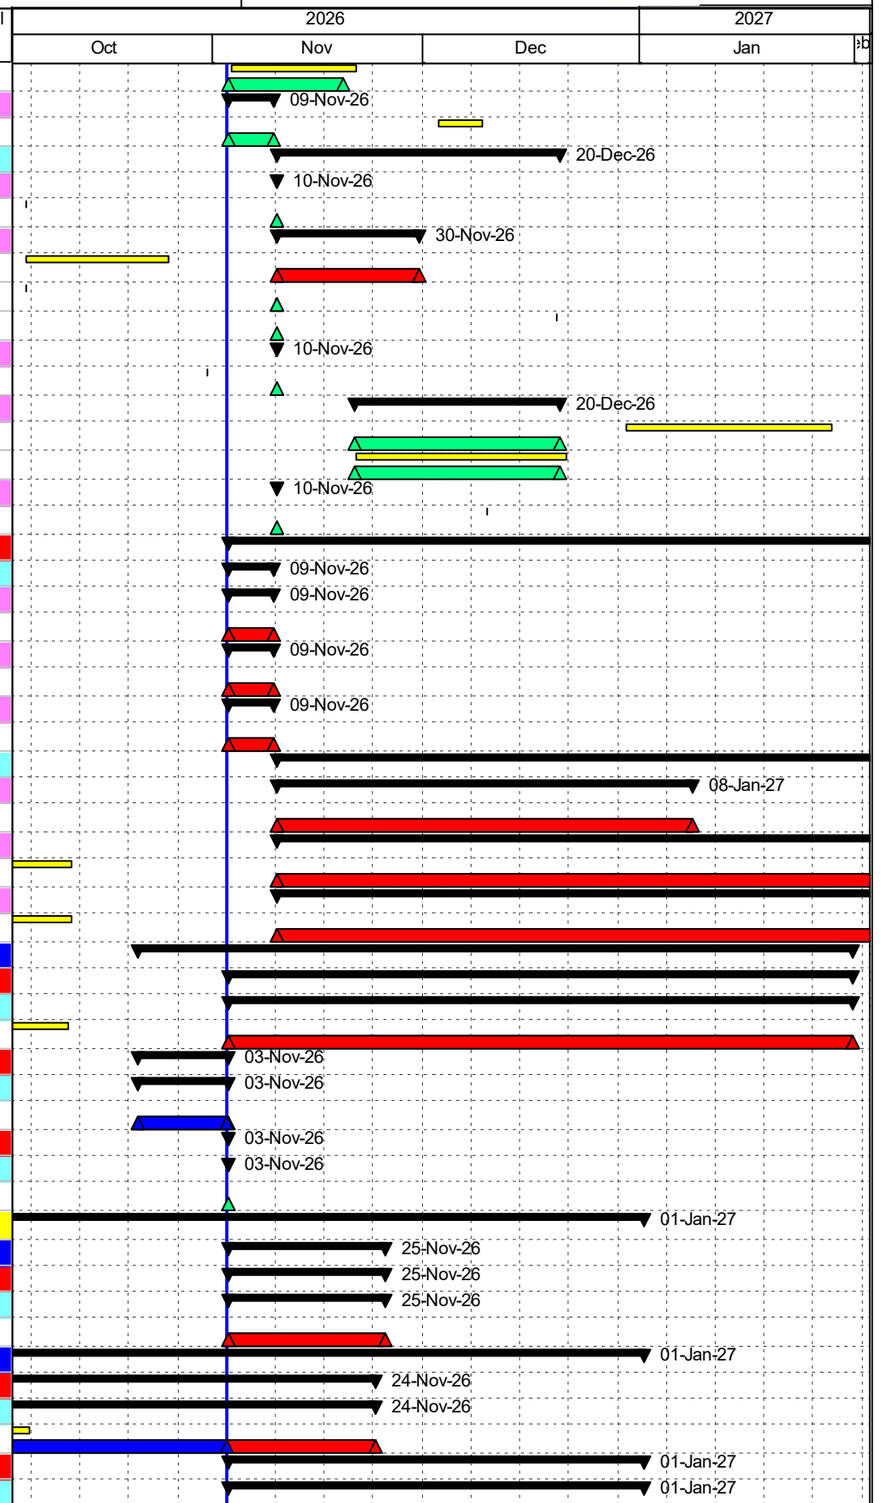


Primary Baseline
Remaining Work
Critical Remaining Work
Actual Work
Baseline Milestone
Milestone
Summary

Date	Revision	Checked	Approved
03-Nov-26	Third Industrial City		

Development of the Technology City in Dammam -Upda
03-11-2026
3Week Lookahead Schedule


Activity ID	Activity Name	Original Duration	Start	Finish	BL Project Start	BL Project Finish	Budgeted Total Cost
PRO-LS-LL-MF-20	Manufacturing of Electromechanical Works for Lift Stations	60	03-Nov-26	01-Jan-27	07-Aug-26	05-Oct-26	0.00
Storage Tank (TSE)		30	03-Nov-26	07-Dec-26	04-Jul-26	06-Aug-26	0.00
Issuance of Purchase Orders		30	03-Nov-26	07-Dec-26	04-Jul-26	06-Aug-26	0.00
PRO-TSE-LL-PO-30	Issuance of Purchase Order for Electromechanical Works for Storage Tank (TSE)	30	03-Nov-26	07-Dec-26	04-Jul-26	06-Aug-26	0.00
Construction Works		217	02-Aug-26 A	13-Mar-27	04-Jul-26	21-Jan-27	19,522,189.79
Infrastructure Networks		178	02-Aug-26 A	17-Jan-27	04-Jul-26	10-Nov-26	5,369,767.01
Earthworks		12	02-Aug-26 A	03-Nov-26	04-Jul-26	16-Jul-26	1,377,108.79
Earthworks		12	02-Aug-26 A	03-Nov-26	04-Jul-26	16-Jul-26	1,377,108.79
CO-EW-200_R	Excavation Works Upto Design Level for Earthworks-P1(Remaining)	10	02-Aug-26 A	03-Nov-26	04-Jul-26	14-Jul-26	522,497.42
CO-EW-210_R	Excavation Works Upto Design Level for Earthworks-P2(Remaining)	10	02-Aug-26 A	03-Nov-26	04-Jul-26	14-Jul-26	275,826.95
CO-EW-220_R	Excavation Works Upto Design Level for Earthworks-P3(Remaining)	12	02-Aug-26 A	03-Nov-26	04-Jul-26	16-Jul-26	578,784.42
Storm Drainage Network		120	02-Aug-26 A	02-Dec-26	15-Jul-26	17-Sep-26	2,959,680.35
FROM MH-25:MH-12		120	02-Aug-26 A	02-Dec-26	15-Jul-26	17-Sep-26	2,553,322.92
Main Line Sections		18	02-Aug-26 A	14-Nov-26	15-Jul-26	04-Aug-26	1,787,972.67
CO-SD-ML-100	Trench Excavation and Bedding Works for Main Lines of Storm Drainage Network	3	02-Aug-26 A	07-Nov-26	15-Jul-26	18-Jul-26	496,659.08
CO-SD-ML-120	Pipes Laying Works for Main Lines of Storm Drainage Network	5	02-Aug-26 A	08-Nov-26	19-Jul-26	23-Jul-26	893,986.33
CO-SD-ML-130	Trench Backfilling and Compaction Works for Main Lines of Storm Drainage Network	10	02-Aug-26 A	14-Nov-26	25-Jul-26	04-Aug-26	397,327.26
Manholes		11	17-Oct-26 A	18-Nov-26	09-Aug-26	06-Sep-26	247,670.25
CO-SD-MH-180	Trench Excavation and Bedding Works for Manholes of Storm Drainage Network	7	17-Oct-26 A	09-Nov-26	09-Aug-26	16-Aug-26	49,534.05
CO-SD-MH-190	Install RC Footing Works for Manholes of Storm Drainage Network	7	29-Oct-26 A	10-Nov-26	17-Aug-26	24-Aug-26	82,556.75
CO-SD-MH-200	Install RC Wall Rings & Slab Works for Manholes of Storm Drainage Network	4	31-Oct-26 A	10-Nov-26	25-Aug-26	29-Aug-26	49,534.05
CO-SD-MH-220	Backfilling Works for Manholes of Storm Drainage Network	7	11-Nov-26	18-Nov-26	30-Aug-26	06-Sep-26	66,045.40
Catch Basin Sections		20	09-Nov-26	02-Dec-26	17-Aug-26	17-Sep-26	517,680.00
CO-SD-CB-140	Trench Excavation and Bedding Works for Catch Basins of Storm Drainage Network	10	09-Nov-26	21-Nov-26	17-Aug-26	27-Aug-26	129,420.00
CO-SD-CB-150	Installation and Pipes Laying Connection Works for Catch Basins of Storm Drainage	10	21-Nov-26	02-Dec-26	07-Sep-26	17-Sep-26	388,260.00
FROM MH-12:MH-01		14	08-Nov-26	23-Nov-26	03-Aug-26	18-Aug-26	406,357.43
Main Line Sections		14	08-Nov-26	23-Nov-26	03-Aug-26	18-Aug-26	406,357.43
CO-SD-ML-140	Trench Excavation and Bedding Works for Main Lines of Storm Drainage Network	14	08-Nov-26	23-Nov-26	03-Aug-26	18-Aug-26	406,357.43
Sewage Network		54	22-Oct-26 A	01-Dec-26	03-Aug-26	29-Sep-26	510,729.48
FROM MH-18:MH-10		54	22-Oct-26 A	25-Nov-26	03-Aug-26	29-Sep-26	249,877.56
Main Line Sections		49	22-Oct-26 A	25-Nov-26	03-Aug-26	22-Sep-26	223,587.36
CO-SW-ML-100	Trench Excavation and Bedding Works for Main Lines of Sewage Network	12	22-Oct-26 A	16-Nov-26	03-Aug-26	16-Aug-26	62,107.60
CO-SW-ML-120	Pipes Laying Works for Main Lines of Sewage Network	12	28-Oct-26 A	16-Nov-26	17-Aug-26	30-Aug-26	111,793.68
CO-SW-ML-130	Trench Backfilling and Compaction Works for Main Lines of Sewage Network	20	31-Oct-26 A	25-Nov-26	31-Aug-26	22-Sep-26	49,686.08
Manholes		25	28-Oct-26 A	16-Nov-26	31-Aug-26	29-Sep-26	26,290.20
CO-SW-MH-160	Excavation Works for Main Line Manholes of Sewage Network	7	28-Oct-26 A	16-Nov-26	31-Aug-26	07-Sep-26	6,572.55
CO-SW-MH-170	Installation RC Footing Works for Main Line Manholes of Sewage Network	7	29-Oct-26 A	16-Nov-26	08-Sep-26	15-Sep-26	8,763.40
CO-SW-MH-180	Install Grp Liner Wall Works for Main Line Manholes of Sewage Network	7	31-Oct-26 A	16-Nov-26	16-Sep-26	24-Sep-26	8,763.40
CO-SW-MH-190	Pouring Grp Liner Wall Works for Main Line Manholes of Sewage Network	4	01-Nov-26 A	16-Nov-26	26-Sep-26	29-Sep-26	2,190.85
FROM MH-10:MH-01		13	16-Nov-26	01-Dec-26	17-Aug-26	31-Aug-26	260,851.92
Main Line Sections		13	16-Nov-26	01-Dec-26	17-Aug-26	31-Aug-26	260,851.92
CO-SW-ML-140	Trench Excavation and Bedding Works for Main Lines of Sewage Network	6	16-Nov-26	23-Nov-26	17-Aug-26	23-Aug-26	93,161.40
CO-SW-ML-150	Pipes Laying Works for Main Lines of Sewage Network	7	23-Nov-26	01-Dec-26	24-Aug-26	31-Aug-26	167,690.52
Potable Water Network		13	21-Oct-26 A	17-Jan-27	14-Oct-26	10-Nov-26	522,248.40
Main Line Sections		13	21-Oct-26 A	17-Jan-27	14-Oct-26	10-Nov-26	522,248.40
CO-PW-ML-100	Trench Excavation and Bedding Works for Main Lines of Potable Water Network	8	21-Oct-26 A	10-Jan-27	14-Oct-26	22-Oct-26	145,069.00
CO-PW-ML-110	Pipes Laying and accessories for Main Lines of Potable Water Network	8	28-Oct-26 A	17-Jan-27	24-Oct-26	01-Nov-26	261,124.20
CO-PW-ML-130	Trench Backfilling and Compaction Works for Main Lines of Potable Water Network	8	30-Oct-26 A	17-Jan-27	02-Nov-26	10-Nov-26	116,055.20
Superstructure Work		181	02-Aug-26 A	13-Mar-27	15-Aug-26	21-Jan-27	14,152,422.77
Utility Buildings		57	23-Sep-26 A	30-Nov-26	10-Sep-26	26-Dec-26	2,451,284.09
Pump Station		20	03-Nov-26	25-Nov-26	02-Dec-26	26-Dec-26	775,846.97
Architectural work		15	03-Nov-26	19-Nov-26	02-Dec-26	20-Dec-26	640,717.32

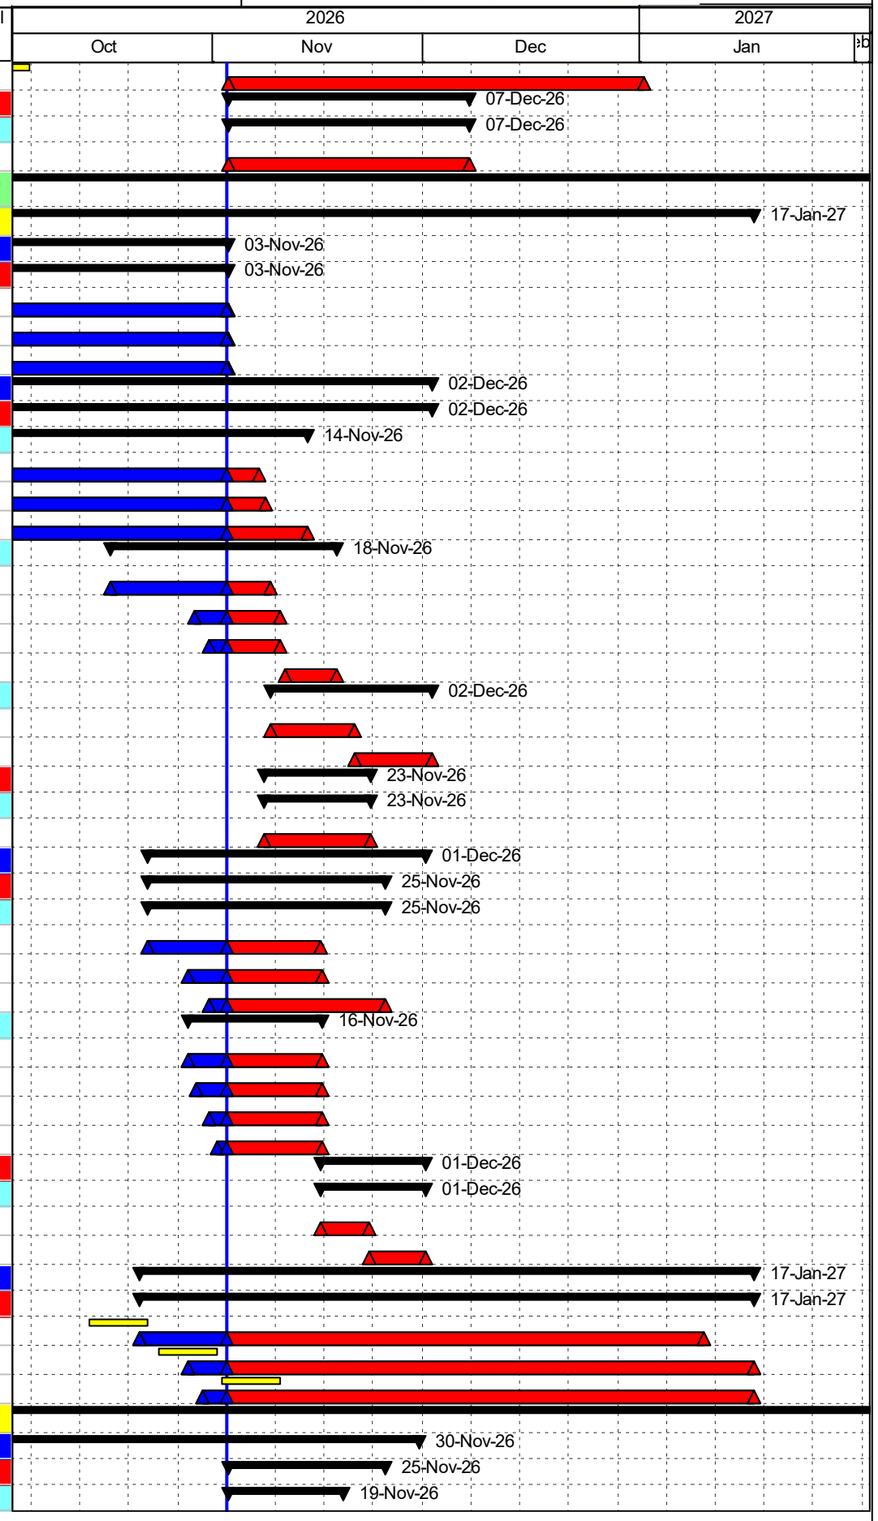

Primary Baseline | Actual Work | Summary
Remaining Work | Baseline Milestone
Critical Remaining Work | Milestone

Date	Revision	Checked	Approved
03-Nov-26	Third Industrial City		

Activity ID	Activity Name	Original Duration	Start	Finish	BL Project Start	BL Project Finish	Budgeted Total Cost
CO-UB-PS-260	Executing Masonry Works for Pump station building	5	03-Nov-26	08-Nov-26	02-Dec-26	08-Dec-26	183,776.32
CO-UB-PS-270	Executing Plastering Works for Pump station building	5	09-Nov-26	14-Nov-26	08-Dec-26	14-Dec-26	229,720.40
CO-UB-PS-280	Executing Painting Works for Pump station building	5	15-Nov-26	19-Nov-26	14-Dec-26	20-Dec-26	227,220.60
Electrical work		5	21-Nov-26	25-Nov-26	20-Dec-26	26-Dec-26	135,129.65
CO-UB-PS-290	Lighting system for pump house	5	21-Nov-26	25-Nov-26	20-Dec-26	26-Dec-26	135,129.65
Lift Station		57	23-Sep-26 A	24-Nov-26	15-Oct-26	24-Nov-26	546,524.36
Civil work		57	23-Sep-26 A	24-Nov-26	15-Oct-26	24-Nov-26	546,524.36
Super structure		57	23-Sep-26 A	24-Nov-26	15-Oct-26	24-Nov-26	546,524.36
CO-UB-LS-290	Formwork for Wall and columns for Lift Station	7	23-Sep-26 A	05-Nov-26	15-Oct-26	22-Oct-26	84,080.67
CO-UB-LS-300	Steel fixing for Wall columns	9	23-Sep-26 A	05-Nov-26	24-Oct-26	02-Nov-26	84,080.67
CO-UB-LS-310	pouring for Wall columns	1	30-Sep-26 A	05-Nov-26	03-Nov-26	03-Nov-26	50,448.40
CO-UB-LS-330	Waterproofing for Walls columns	4	08-Oct-26 A	10-Nov-26	07-Nov-26	10-Nov-26	84,080.67
CO-UB-LS-320	curing and deshuttering formwork for Wall columns	2	17-Oct-26 A	08-Nov-26	04-Nov-26	05-Nov-26	8,408.07
CO-UB-LS-340	Formwork for pump roof	5	10-Nov-26	16-Nov-26	11-Nov-26	16-Nov-26	84,080.67
CO-UB-LS-350	Steel fixing for pump roof	6	16-Nov-26	23-Nov-26	17-Nov-26	23-Nov-26	84,080.67
CO-UB-LS-360	pouring for pump roof	1	23-Nov-26	24-Nov-26	24-Nov-26	24-Nov-26	67,264.53
Potable Water Tank		18	03-Nov-26	23-Nov-26	10-Sep-26	01-Oct-26	176,265.75
Structural Work		12	03-Nov-26	16-Nov-26	10-Sep-26	24-Sep-26	93,641.18
CO-UB-PWT-130	Form work for Tank Foundation	5	03-Nov-26	08-Nov-26	10-Sep-26	15-Sep-26	41,312.28
CO-UB-PWT-140	Steel Reinforcement work for Tank Foundation	6	09-Nov-26	15-Nov-26	16-Sep-26	22-Sep-26	38,558.13
CO-UB-PWT-150	Casting concrete for Tank Foundation	1	16-Nov-26	16-Nov-26	24-Sep-26	24-Sep-26	13,770.76
Tank Shell Erection&Roof Installation		6	17-Nov-26	23-Nov-26	26-Sep-26	01-Oct-26	82,624.57
CO-UB-PWT-160	Bottom ring installation	6	17-Nov-26	23-Nov-26	26-Sep-26	01-Oct-26	82,624.57
IrrigationTank		18	03-Nov-26	23-Nov-26	26-Nov-26	16-Dec-26	176,265.75
Structural Work		12	03-Nov-26	16-Nov-26	26-Nov-26	09-Dec-26	93,641.18
CO-UB-IRT-170	Form work for Tank Foundation	6	03-Nov-26	09-Nov-26	26-Nov-26	02-Dec-26	41,312.28
CO-UB-IRT-180	Steel Reinforcement work for Tank Foundation	5	10-Nov-26	15-Nov-26	03-Dec-26	08-Dec-26	38,558.13
CO-UB-IRT-190	Casting concrete for Tank Foundation	1	16-Nov-26	16-Nov-26	09-Dec-26	09-Dec-26	13,770.76
Tank Shell Erection&Roof Installation		6	17-Nov-26	23-Nov-26	10-Dec-26	16-Dec-26	82,624.57
CO-UB-IRT-200	Bottom ring installation	6	17-Nov-26	23-Nov-26	10-Dec-26	16-Dec-26	82,624.57
Control Room		28	24-Oct-26 A	30-Nov-26	28-Oct-26	03-Dec-26	776,381.28
Civil Work		8	24-Oct-26 A	03-Nov-26	28-Oct-26	05-Nov-26	252,242.01
CO-UB-CR-140	Pouring Beams and Slab For Control Room	8	24-Oct-26 A	03-Nov-26	28-Oct-26	05-Nov-26	252,242.01
Finishing Work		24	03-Nov-26	30-Nov-26	07-Nov-26	03-Dec-26	524,139.27
Architictural work		24	03-Nov-26	30-Nov-26	07-Nov-26	03-Dec-26	288,276.60
CO-UB-CR-150	Brick Work For Control Room	9	03-Nov-26	12-Nov-26	07-Nov-26	16-Nov-26	96,092.20
CO-UB-CR-160	Thermal & Moisture Protection Work for Control Room	7	14-Nov-26	21-Nov-26	17-Nov-26	24-Nov-26	96,092.20
CO-UB-CR-200	Install For Curtian Wall and Windows and Doors	8	22-Nov-26	30-Nov-26	25-Nov-26	03-Dec-26	96,092.20
Mechanical Work		8	14-Nov-26	22-Nov-26	17-Nov-26	25-Nov-26	192,184.40
HVAC System		4	14-Nov-26	17-Nov-26	17-Nov-26	21-Nov-26	96,092.20
CO-UB-CR-170	Install of Refrigerant Piping (fabricated metal ducts with flanges complete with suppo	4	14-Nov-26	17-Nov-26	17-Nov-26	21-Nov-26	96,092.20
Fire Fitting System		4	18-Nov-26	22-Nov-26	22-Nov-26	25-Nov-26	96,092.20
CO-UB-CR-180	Installation & Testing of 2 hours Fire rated system for closing the openings between r	4	18-Nov-26	22-Nov-26	22-Nov-26	25-Nov-26	96,092.20
Electrical Work		5	23-Nov-26	28-Nov-26	26-Nov-26	01-Dec-26	43,678.27
Fire Detection And Alarm System		5	23-Nov-26	28-Nov-26	26-Nov-26	01-Dec-26	43,678.27
CO-UB-CR-210	Install of 2C x 1.5 Sqm FR Rated Armored - Cable For Loop Wiring	5	23-Nov-26	28-Nov-26	26-Nov-26	01-Dec-26	43,678.27
Fence and Gaurd Room		181	02-Aug-26 A	13-Mar-27	15-Aug-26	21-Jan-27	11,701,138.68
Gaurd Room Work		56	25-Oct-26 A	26-Nov-26	10-Sep-26	05-Oct-26	73,200.00
Civil Work		56	25-Oct-26 A	26-Nov-26	10-Sep-26	05-Oct-26	73,200.00
A1020	Pouring R.C Footing For Gaurd Room	11	25-Oct-26 A	15-Nov-26	10-Sep-26	22-Sep-26	60,600.00
A1030	Pouring R.C Columns For Gaurd Room	10	16-Nov-26	26-Nov-26	24-Sep-26	05-Oct-26	12,600.00
Fence Work		181	02-Aug-26 A	13-Mar-27	15-Aug-26	21-Jan-27	11,627,938.68
Northern Fence N01:N03		44	21-Oct-26 A	01-Dec-26	29-Aug-26	09-Nov-26	2,154,000.47

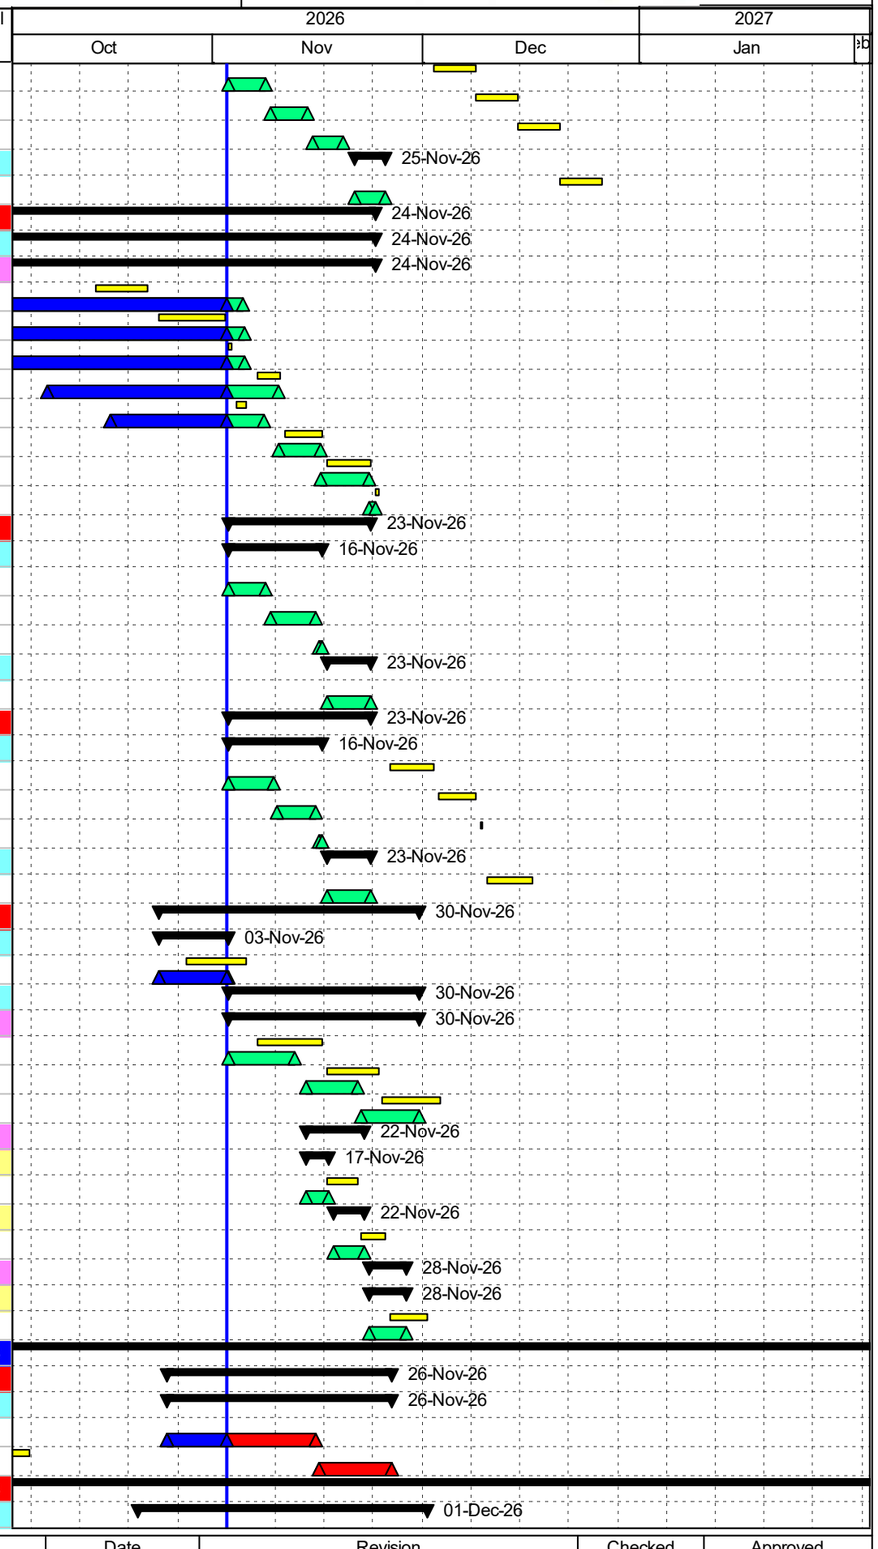


Primary Baseline | Actual Work | Summary
Remaining Work | Baseline Milestone
Critical Remaining Work | Milestone

Date	Revision	Checked	Approved
03-Nov-26	Third Industrial City		

Development of the Technology City in Dammam -Upda
03-11-2026
3Week Lookahead Schedule

Activity ID	Activity Name	Original Duration	Start	Finish	BL Project Start	BL Project Finish	Budgeted Total Cost
Finishing Work		44	21-Oct-26 A	01-Dec-26	29-Aug-26	09-Nov-26	2,154,000.47
Electrical Work		25	03-Nov-26	01-Dec-26	29-Aug-26	27-Sep-26	43,078.18
CO-SU-FE-N-EL-	Trench excavation to receive 2 nos 50mm diameter PVC Conduit	8	03-Nov-26	11-Nov-26	29-Aug-26	06-Sep-26	17,843.64
CO-SU-FE-N-EL-	Trench excavation to receive 3 nos 50mm diameter PVC Conduit	8	03-Nov-26	11-Nov-26	29-Aug-26	06-Sep-26	8,181.82
CO-SU-FE-N-EL-	Fixing of Control cable,CAT6A cable	9	12-Nov-26	22-Nov-26	07-Sep-26	16-Sep-26	4,240.91
CO-SU-FE-N-EL-	Install 800mm x 800mm x 800mm height concrete handhole	9	12-Nov-26	22-Nov-26	07-Sep-26	16-Sep-26	4,435.64
CO-SU-FE-N-EL-	Hot dipped galvanized cable conduits for CAT6A cable and Control Cables embedde	8	12-Nov-26	21-Nov-26	07-Sep-26	15-Sep-26	5,767.36
CO-SU-FE-N-EL-	Fixing Earthing Work (Earth Pit,Grounding rod,Tinned Copper wire)	8	23-Nov-26	01-Dec-26	17-Sep-26	27-Sep-26	2,608.82
Architictural work		37	21-Oct-26 A	10-Nov-26	18-Oct-26	09-Nov-26	2,110,922.29
CO-SU-FE-N-AR-	External plastering to walls and columns	7	21-Oct-26 A	08-Nov-26	18-Oct-26	25-Oct-26	0.00
CO-SU-FE-N-AR-	Install 50mm thick random cut stone cladding	7	22-Oct-26 A	10-Nov-26	26-Oct-26	02-Nov-26	2,046,910.47
CO-SU-FE-N-AR-	Install 2 coats of weatherproof paint at walls	6	28-Oct-26 A	10-Nov-26	03-Nov-26	09-Nov-26	64,011.82
Western Fence P1 (W01:W06)		106	17-Sep-26 A	28-Nov-26	12-Sep-26	11-Jan-27	1,799,880.58
Civil Work		28	17-Sep-26 A	07-Nov-26	12-Sep-26	01-Nov-26	757,243.64
CO-SU-FE-WP1-C	Pouring R.C Columns For Northern Fence	16	17-Sep-26 A	04-Nov-26	12-Sep-26	01-Oct-26	675,381.82
CO-SU-FE-WP1-C	Pouring Beams For Northern Fence	17	05-Oct-26 A	07-Nov-26	12-Oct-26	01-Nov-26	81,861.82
Finishing Work		87	29-Sep-26 A	28-Nov-26	01-Oct-26	11-Jan-27	1,042,636.95
Electrical Work		14	12-Nov-26	28-Nov-26	12-Oct-26	28-Oct-26	52,050.91
CO-SU-FE-WP1-E	Trench excavation to receive 2 nos 50mm diameter PVC Conduit	14	12-Nov-26	28-Nov-26	12-Oct-26	28-Oct-26	35,687.27
CO-SU-FE-WP1-E	Trench excavation to receive 3 nos 50mm diameter PVC Conduit	14	12-Nov-26	28-Nov-26	12-Oct-26	28-Oct-26	16,363.64
Architictural work		87	29-Sep-26 A	17-Nov-26	01-Oct-26	11-Jan-27	990,586.04
CO-SU-FE-WP1-A	Install Brick Work For Northern Fence	9	29-Sep-26 A	07-Nov-26	01-Oct-26	12-Oct-26	317,018.18
CO-SU-FE-WP1-A	External plastering to walls and columns	6	22-Oct-26 A	10-Nov-26	19-Dec-26	24-Dec-26	0.00
CO-SU-FE-WP1-A	Install 50mm thick random cut stone cladding	5	24-Oct-26 A	10-Nov-26	26-Dec-26	30-Dec-26	397,484.95
CO-SU-FE-WP1-A	Install 2 coats of weatherproof paint at walls	6	28-Oct-26 A	12-Nov-26	31-Dec-26	06-Jan-27	128,023.64
CO-SU-FE-WP1-A	Install Stone coping 500mm,525mm	4	12-Nov-26	17-Nov-26	07-Jan-27	11-Jan-27	148,059.27
Western Fence P2 (W07:W12)		69	19-Sep-26 A	10-Dec-26	07-Oct-26	30-Dec-26	2,585,719.77
Civil Work		36	19-Sep-26 A	07-Nov-26	07-Oct-26	09-Nov-26	649,036.64
CO-SU-FE-WP2-C	Pouring R.C Columns For Northern Fence	9	19-Sep-26 A	03-Nov-26	07-Oct-26	18-Oct-26	567,174.83
CO-SU-FE-WP2-C	Pouring Beams For Northern Fence	7	11-Oct-26 A	07-Nov-26	01-Nov-26	09-Nov-26	81,861.82
Finishing Work		55	29-Sep-26 A	10-Dec-26	18-Oct-26	30-Dec-26	1,936,683.13
Electrical Work		19	04-Nov-26	26-Nov-26	27-Oct-26	18-Nov-26	86,156.36
CO-SU-FE-WP2-E	Trench excavation to receive 2 nos 50mm diameter PVC Conduit	4	04-Nov-26	09-Nov-26	27-Oct-26	01-Nov-26	35,687.27
CO-SU-FE-WP2-E	Trench excavation to receive 3 nos 50mm diameter PVC Conduit	6	04-Nov-26	11-Nov-26	27-Oct-26	03-Nov-26	16,363.64
CO-SU-FE-WP2-E	Fixing of Control cable,CAT6A cable	7	11-Nov-26	19-Nov-26	03-Nov-26	11-Nov-26	8,481.82
CO-SU-FE-WP2-E	Install 800mm x 800mm x 800mm height concrete handhole	7	11-Nov-26	19-Nov-26	03-Nov-26	10-Nov-26	8,871.27
CO-SU-FE-WP2-E	Hot dipped galvanized cable conduits for CAT6A cable and Control Cables embedde	6	11-Nov-26	18-Nov-26	03-Nov-26	10-Nov-26	11,534.73
CO-SU-FE-WP2-E	Fixing Earthing Work (Earth Pit,Grounding rod,Tinned Copper wire)	6	19-Nov-26	26-Nov-26	11-Nov-26	18-Nov-26	5,217.64
Architictural work		55	29-Sep-26 A	10-Dec-26	18-Oct-26	30-Dec-26	1,850,526.76
CO-SU-FE-WP2-A	Install Brick Work For Northern Fence	8	29-Sep-26 A	04-Nov-26	18-Oct-26	27-Oct-26	317,018.18
CO-SU-FE-WP2-A	External plastering to walls and columns	8	28-Oct-26 A	10-Dec-26	02-Dec-26	12-Dec-26	0.00
CO-SU-FE-WP2-A	Install 50mm thick random cut stone cladding	8	28-Oct-26 A	10-Dec-26	12-Dec-26	21-Dec-26	1,405,484.95
CO-SU-FE-WP2-A	Install 2 coats of weatherproof paint at walls	8	28-Oct-26 A	10-Dec-26	21-Dec-26	30-Dec-26	128,023.64
Southern Fence S01:S05		181	02-Aug-26 A	13-Mar-27	15-Aug-26	07-Jan-27	2,215,400.76
Civil Work		73	02-Aug-26 A	05-Nov-26	15-Aug-26	14-Sep-26	1,777,083.64
CO-SU-FE-S-CI-27	Pouring R.C Footing For Northern Fence	8	02-Aug-26 A	04-Nov-26	15-Aug-26	23-Aug-26	990,000.00
CO-SU-FE-S-CI-28	Pouring R.C Columns For Northern Fence	10	05-Oct-26 A	04-Nov-26	24-Aug-26	03-Sep-26	718,865.45
CO-SU-FE-S-CI-29	Pouring Beams For Northern Fence	9	08-Oct-26 A	05-Nov-26	05-Sep-26	14-Sep-26	68,218.18
Finishing Work		123	29-Sep-26 A	13-Mar-27	05-Sep-26	07-Jan-27	438,317.12
Electrical Work		30	03-Nov-26	07-Dec-26	05-Sep-26	10-Oct-26	67,448.94
CO-SU-FE-S-EL-5	Trench excavation to receive 2 nos 50mm diameter PVC Conduit	15	03-Nov-26	19-Nov-26	05-Sep-26	21-Sep-26	29,739.39
CO-SU-FE-S-EL-6	Trench excavation to receive 3 nos 50mm diameter PVC Conduit	15	03-Nov-26	19-Nov-26	05-Sep-26	21-Sep-26	13,636.36

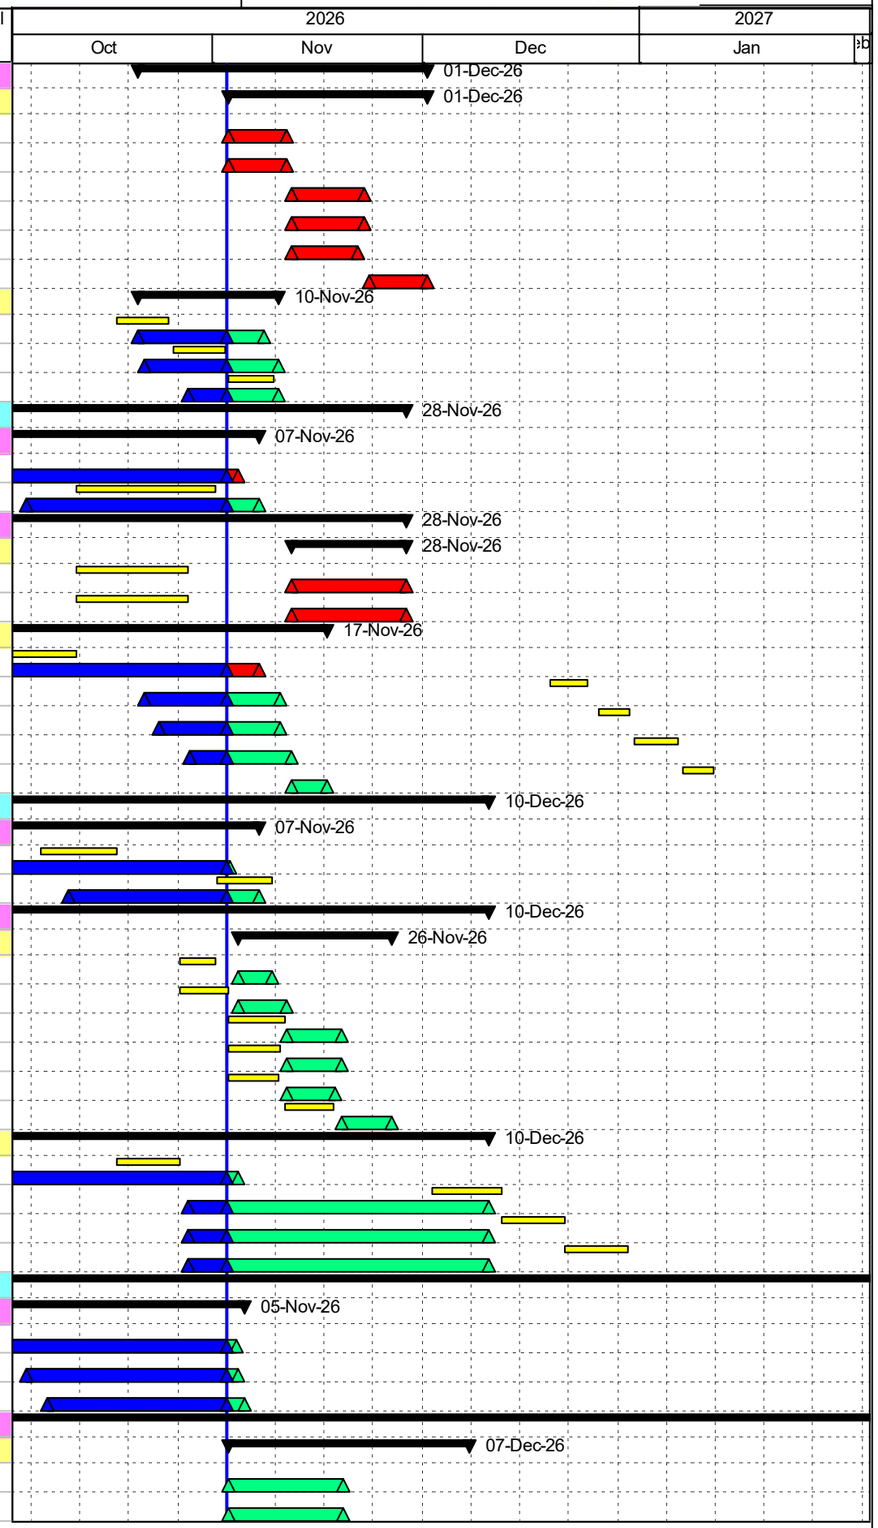


Primary Baseline | Actual Work | Summary
Remaining Work | Baseline Milestone
Critical Remaining Work | Milestone

Date	Revision	Checked	Approved
03-Nov-26	Third Industrial City		

Development of the Technology City in Dammam -Upda
03-11-2026
3Week Lookahead Schedule

Activity ID	Activity Name	Original Duration	Start	Finish	BL Project Start	BL Project Finish	Budgeted Total Cost
CO-SU-FE-S-EL-(	Fixing of Control cable,CAT6A cable	15	21-Nov-26	07-Dec-26	22-Sep-26	10-Oct-26	7,068.18
CO-SU-FE-S-EL-(	Install 800mm x 800mm x 800mm height concrete handhole	15	21-Nov-26	07-Dec-26	22-Sep-26	10-Oct-26	7,392.73
CO-SU-FE-S-EL-(	Hot dipped galvanized cable conduits for CAT6A cable and Control Cables embedde	15	21-Nov-26	07-Dec-26	22-Sep-26	10-Oct-26	9,612.27
Architictural work		123	29-Sep-26 A	13-Mar-27	05-Sep-26	07-Jan-27	370,868.18
CO-SU-FE-S-AR-:	Install Brick Work For Northern Fence	6	29-Sep-26 A	07-Nov-26	05-Sep-26	10-Sep-26	264,181.82
CO-SU-FE-S-AR-:	External plastering to walls and columns	6	28-Oct-26 A	22-Dec-26	26-Oct-26	01-Nov-26	0.00
CO-SU-FE-S-AR-:	Install 2 coats of weatherproof paint at walls	8	28-Oct-26 A	13-Mar-27	30-Dec-26	07-Jan-27	106,686.36
Eastern Fence P1 (E01:E06)		67	29-Sep-26 A	13-Dec-26	21-Sep-26	15-Dec-26	1,697,359.49
Civil Work		22	06-Oct-26 A	08-Nov-26	21-Sep-26	26-Oct-26	600,676.36
CO-SU-FE-EP1-CI	Pouring R.C Columns For Northern Fence	15	06-Oct-26 A	08-Nov-26	21-Sep-26	08-Oct-26	518,814.55
CO-SU-FE-EP1-CI	Pouring Beams For Northern Fence	7	08-Oct-26 A	08-Nov-26	19-Oct-26	26-Oct-26	81,861.82
Finishing Work		58	29-Sep-26 A	13-Dec-26	10-Oct-26	15-Dec-26	1,096,683.13
Electrical Work		14	08-Nov-26	24-Nov-26	19-Oct-26	03-Nov-26	86,156.36
CO-SU-FE-EP1-E	Trench excavation to receive 2 nos 50mm diameter PVC Conduit	4	08-Nov-26	12-Nov-26	19-Oct-26	22-Oct-26	35,687.27
CO-SU-FE-EP1-E	Trench excavation to receive 3 nos 50mm diameter PVC Conduit	4	08-Nov-26	12-Nov-26	19-Oct-26	22-Oct-26	16,363.64
CO-SU-FE-EP1-E	Fixing of Control cable,CAT6A cable	4	12-Nov-26	17-Nov-26	24-Oct-26	27-Oct-26	8,481.82
CO-SU-FE-EP1-E	Install 800mm x 800mm x 800mm height concrete handhole	4	12-Nov-26	17-Nov-26	24-Oct-26	27-Oct-26	8,871.27
CO-SU-FE-EP1-E	Hot dipped galvanized cable conduits for CAT6A cable and Control Cables embedde	4	12-Nov-26	17-Nov-26	24-Oct-26	27-Oct-26	11,534.73
CO-SU-FE-EP1-E	Fixing Earthing Work (Earth Pit,Grounding rod,Tinned Copper wire)	6	17-Nov-26	24-Nov-26	28-Oct-26	03-Nov-26	5,217.64
Architictural work		58	29-Sep-26 A	13-Dec-26	10-Oct-26	15-Dec-26	1,010,526.76
CO-SU-FE-EP1-A	Install Brick Work For Northern Fence	8	29-Sep-26 A	08-Nov-26	10-Oct-26	18-Oct-26	317,018.18
CO-SU-FE-EP1-A	Install 50mm thick random cut stone cladding	10	28-Oct-26 A	13-Dec-26	23-Nov-26	03-Dec-26	565,484.95
CO-SU-FE-EP1-A	Install 2 coats of weatherproof paint at walls	10	28-Oct-26 A	13-Dec-26	05-Dec-26	15-Dec-26	128,023.64
Eastern Fence P2 (E07:E13)		91	15-Sep-26 A	26-Jan-27	03-Nov-26	21-Jan-27	1,175,577.61
Civil Work		43	15-Sep-26 A	11-Nov-26	03-Nov-26	02-Dec-26	571,829.09
CO-SU-FE-EP2-CI	Pouring R.C Columns For Northern Fence	10	15-Sep-26 A	08-Nov-26	03-Nov-26	14-Nov-26	476,323.64
CO-SU-FE-EP2-CI	Pouring Beams For Northern Fence	10	01-Oct-26 A	11-Nov-26	22-Nov-26	02-Dec-26	95,505.45
Finishing Work		77	29-Sep-26 A	26-Jan-27	15-Nov-26	21-Jan-27	603,748.52
Electrical Work		7	09-Nov-26	17-Nov-26	22-Nov-26	29-Nov-26	84,533.06
CO-SU-FE-EP2-E	Trench excavation to receive 2 nos 50mm diameter PVC Conduit	4	09-Nov-26	14-Nov-26	22-Nov-26	25-Nov-26	41,635.15
CO-SU-FE-EP2-E	Trench excavation to receive 3 nos 50mm diameter PVC Conduit	4	09-Nov-26	14-Nov-26	22-Nov-26	25-Nov-26	19,090.91
CO-SU-FE-EP2-E	Install 800mm x 800mm x 800mm height concrete handhole	3	14-Nov-26	17-Nov-26	26-Nov-26	29-Nov-26	10,349.82
CO-SU-FE-EP2-E	Hot dipped galvanized cable conduits for CAT6A cable and Control Cables embedde	3	14-Nov-26	17-Nov-26	26-Nov-26	29-Nov-26	13,457.18
Architictural work		56	29-Sep-26 A	26-Jan-27	15-Nov-26	21-Jan-27	519,215.45
CO-SU-FE-EP2-A	Install Brick Work For Northern Fence	6	29-Sep-26 A	09-Nov-26	15-Nov-26	21-Nov-26	369,854.55
CO-SU-FE-EP2-A	External plastering to walls and columns	5	28-Oct-26 A	20-Jan-27	04-Jan-27	10-Jan-27	0.00
CO-SU-FE-EP2-A	Install 2 coats of weatherproof paint at walls	5	28-Oct-26 A	26-Jan-27	16-Jan-27	21-Jan-27	149,360.91
Testing and Comissioning		0	03-Nov-26	03-Nov-26	04-Jan-27	04-Jan-27	0.00
Utility Buildings		0	03-Nov-26	03-Nov-26	04-Jan-27	04-Jan-27	0.00
T/C-DPO	Testing and Commissioning of Storm Drainage Ponds	0	03-Nov-26	03-Nov-26	04-Jan-27	04-Jan-27	0.00
Handing over and close out		14	03-Nov-26	18-Nov-26	04-Jan-27	19-Jan-27	0.00
As-Built		14	03-Nov-26	18-Nov-26	04-Jan-27	19-Jan-27	0.00
HO-130	Submission As-Built Drawing For Pond	14	03-Nov-26	18-Nov-26	04-Jan-27	19-Jan-27	0.00

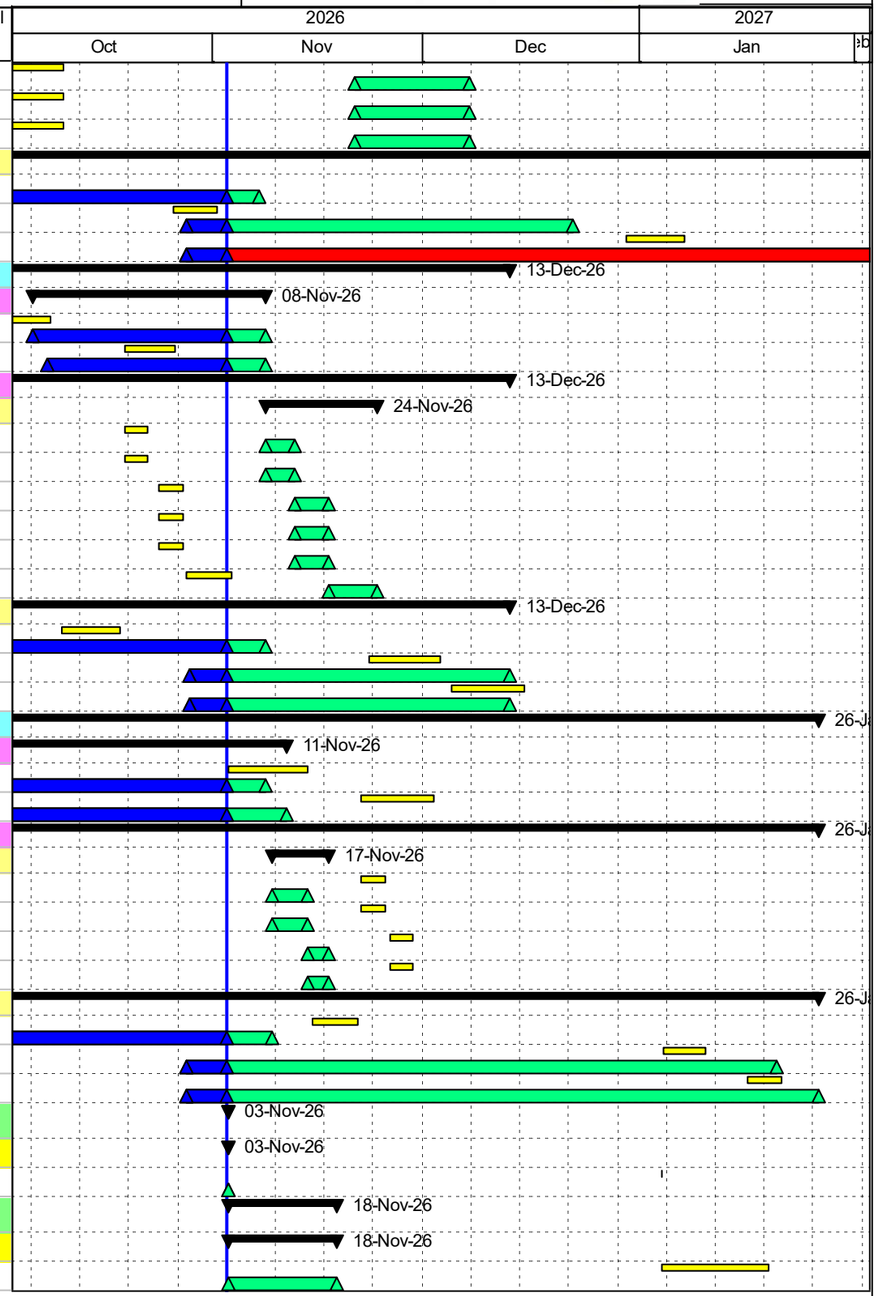

Primary Baseline
Remaining Work
Critical Remaining Work
Actual Work
Baseline Milestone
Milestone
Summary

Date	Revision	Checked	Approved
03-Nov-26	Third Industrial City		
