
Infrastructure Works of Area J -3rd Industrial City-Dammam-Phase 2 - Update 13-10-2026

WPR UPS LEVEL 5

Activity ID	Activity Name	Original Duration	BL Project Start	BL Project Finish	Start	Finish	BL Project Total Cost	Earned Value Cost	Schedule % Complete	Performance % Complete
Infrastructure Works of Area J -3rd Industrial City-Dammam-Phase 2 - U		892	12-Jan-25	11-Jan-27	12-Jan-25 A	20-Dec-27	117,391,774	88,058,371	84.51%	75.01%
Key Milestones		892	12-Jan-25	11-Jan-27	12-Jan-25 A	20-Dec-27	0	0	0%	0%
Contractual Milestones		892	12-Jan-25	11-Jan-27	12-Jan-25 A	20-Dec-27	0	0	0%	0%
MS-CF-IR	Completion of Construction Works for Irrigation Network	0		28-Oct-26		22-Jul-27*	0	0	0%	0%
MS-CF-MV	Completion of Construction Works for Medium Voltage Network	0		28-Oct-26		23-Mar-27*	0	0	0%	0%
MS-CF-PW	Completion of Construction Works for Potable Water Network	0		18-Nov-26		04-Oct-27*	0	0	0%	0%
MS-CF-RD	Completion of Construction Works for Road Works	0		28-Dec-26		06-Dec-27	0	0	0%	0%
MS-CF-SW	Completion of Construction Works for Sewage Network	0		08-Nov-26		12-Aug-27*	0	0	0%	0%
MS-CF-SD	Completion of Construction Works for Storm Drainage Network	0		12-Dec-26		01-Sep-27*	0	0	0%	0%
MS-CF-SL	Completion of Construction Works for Street Lighting Network	0		15-Oct-26		03-Oct-27*	0	0	0%	0%
MS-CF-TE	Completion of Construction Works for Telecom Network	0		01-Sep-26		10-May-27*	0	0	100%	0%
MS-CF-MOB	Completion of Mobilization Works	0		09-Mar-25		09-Mar-25 A	0	0	100%	100%
MS-CF-ENG	Completion of Submitting and Approval of Shopdrwing and Material	0		10-Feb-25		24-May-25 A	0	0	100%	100%
MS-CF-EBL	Completion of Work Plan and Baseline Schedule	0		10-Feb-25		10-Mar-25 A	0	0	100%	100%
MS-CS-PS	Project Commencement Date (Site Handover)	0	12-Jan-25		12-Jan-25 A		0	0	100%	100%
MS-CF-PF	Project Completion Date	0		11-Jan-27		20-Dec-27	0	0	0%	0%
Control Milestones		439	09-Jul-25	21-Jun-26	29-Apr-25 A	14-Dec-26	0	0	0%	0%
MS-CS-IR	The Employer Approval NOC for Irrigation Network	0	19-Nov-25		16-Jun-25 A		0	0	100%	100%
MS-CS-MV	The Employer Approval NOC for Medium Voltage Network	0	14-Feb-26		14-Dec-26		0	0	100%	0%
MS-CS-PW	The Employer Approval NOC for Potable Water Network	0	03-Nov-25		19-Jun-25 A		0	0	100%	100%
MS-CS-RD	The Employer Approval NOC for Roads Works	0	21-Jun-26		10-Jul-25 A		0	0	100%	100%
MS-CS-SW	The Employer Approval NOC for Sewage Network	0	09-Jul-25		29-Apr-25 A		0	0	100%	100%
MS-CS-SD	The Employer Approval NOC for Storm Drainage Network	0	08-Sep-25		30-Apr-25 A		0	0	100%	100%
MS-CS-SL	The Employer Approval NOC for Street Lighting Network	0	29-Dec-25		08-Jul-25 A		0	0	100%	100%
MS-CS-TE	The Employer Approval NOC for Telecom Network	0	03-May-26		08-Jul-25 A		0	0	100%	100%
Intermediate Milestones		148	24-Aug-26	28-Dec-26	15-Jun-27	06-Dec-27	0	0	0%	0%
MS-MO-10	Completion of Sewage Pump Stations	0		01-Dec-26		15-Jun-27	0	0	0%	0%
MS-MO-30	Completion of Tie In To Existing Networks	0		28-Dec-26		06-Dec-27	0	0	0%	0%
MS-MO-20	Completion of Storm Drainage Ponds	0		24-Aug-26		02-Aug-27	0	0	100%	0%
Preliminaries and Mobilization Works		48	12-Jan-25	09-Mar-25	12-Jan-25 A	12-Mar-25 A	0	0	0%	0%
Mobilization Works		48	12-Jan-25	09-Mar-25	12-Jan-25 A	12-Mar-25 A	0	0	0%	0%
MOB-10	Clear and Grub for Offices and Access Roads	24	12-Jan-25	08-Feb-25	12-Jan-25 A	12-Mar-25 A	0	0	100%	100%
MOB-40	Construction Project Store & Temporary Fence	24	09-Feb-25	09-Mar-25	09-Feb-25 A	12-Mar-25 A	0	0	100%	100%
MOB-80	Construction Site Access Roads	24	09-Feb-25	09-Mar-25	09-Feb-25 A	12-Mar-25 A	0	0	100%	100%
MOB-70	Installation Project Sign Board	24	09-Feb-25	09-Mar-25	09-Feb-25 A	12-Mar-25 A	0	0	100%	100%
MOB-60	Mobilization of Major Equipments	24	09-Feb-25	09-Mar-25	09-Feb-25 A	12-Mar-25 A	0	0	100%	100%
MOB-50	Mobilization of Major Manpower	24	09-Feb-25	09-Mar-25	09-Feb-25 A	12-Mar-25 A	0	0	100%	100%

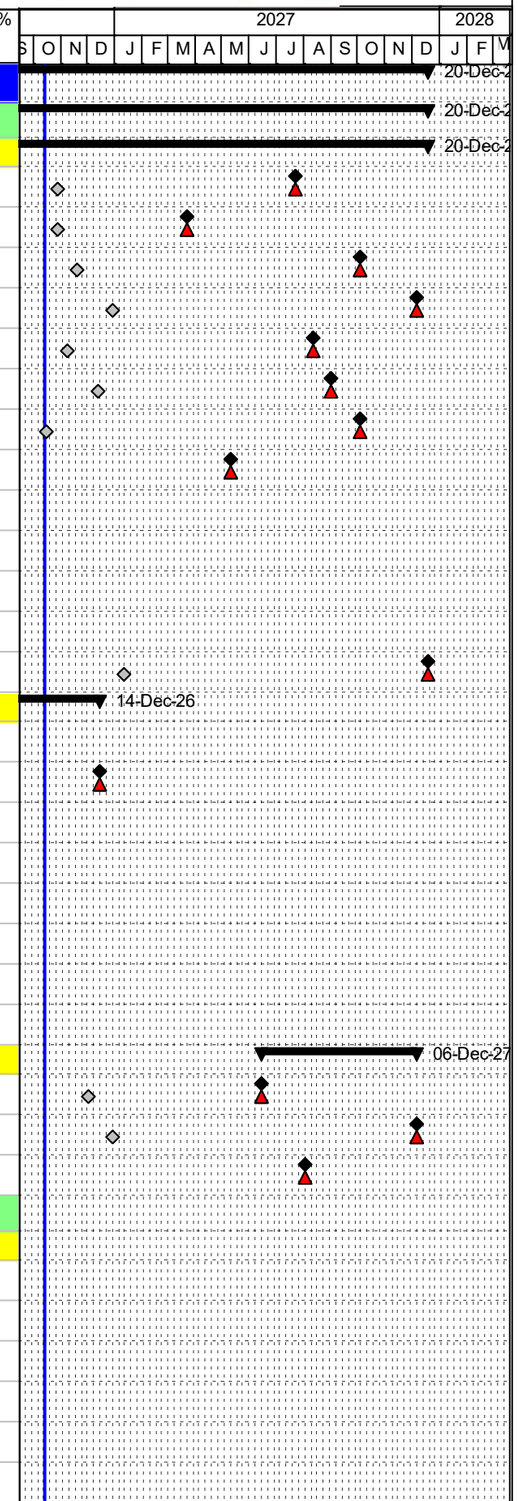


Primary Baseline | Actual Work | Summary

Remaining Work | Baseline Milestone

Critical Remaining Work | Milestone

Date	Revision	Checked	Approved
13-Oct-26	Third Industrial City		


Activity ID	Activity Name	Original Duration	BL Project Start	BL Project Finish	Start	Finish	BL Project Total Cost	Earned Value Cost	Schedule % Complete	Performance % Complete
MOB-20	Project Site Layout Plan Approval	24	12-Jan-25	08-Feb-25	12-Jan-25 A	12-Mar-25 A	0	0	100%	100%
MOB-30	Supply & Install of Project Supervision Offices	24	09-Feb-25	09-Mar-25	09-Feb-25 A	12-Mar-25 A	0	0	100%	100%
Project Documents Provision From The Employer		0	12-Jan-25	12-Jan-25	12-Jan-25 A	12-Feb-25 A	0	0	0%	0%
PRE-EMP-MDC-1	Receive of Approved Project Master Plans of works (IFC) From The Employer	0	12-Jan-25		12-Jan-25 A		0	0	100%	100%
PRE-EMP-MDC-2	Receive of Site Benchmark Coordinates (Original Point) From The Employer	0	12-Jan-25		12-Feb-25 A		0	0	100%	100%
PRE-EMP-MDC-3	Receive of Site Surveying Details From The Employer	0	12-Jan-25		12-Feb-25 A		0	0	100%	100%
Project Main Documents From The Contractor		26	12-Jan-25	10-Feb-25	12-Jan-25 A	02-Mar-25 A	0	0	0%	0%
PRE-CON-MDC-2	Submission Project Baseline Schedule	26	12-Jan-25	10-Feb-25	12-Jan-25 A	01-Mar-25 A	0	0	100%	100%
PRE-CON-MDC-7	Submission Project Environmental Plan	26	12-Jan-25	10-Feb-25	12-Jan-25 A	02-Mar-25 A	0	0	100%	100%
PRE-CON-MDC-6	Submission Project Geotechnical Soil Report	26	12-Jan-25	10-Feb-25	12-Jan-25 A	02-Mar-25 A	0	0	100%	100%
PRE-CON-MDC-3	Submission Project Health & Safety Plan	26	12-Jan-25	10-Feb-25	12-Jan-25 A	02-Mar-25 A	0	0	100%	100%
PRE-CON-MDC-8	Submission Project Organization Chart and Communications Plan	26	12-Jan-25	10-Feb-25	12-Jan-25 A	02-Mar-25 A	0	0	100%	100%
PRE-CON-MDC-4	Submission Project Quality Control Plan	26	12-Jan-25	10-Feb-25	12-Jan-25 A	02-Mar-25 A	0	0	100%	100%
PRE-CON-MDC-5	Submission Project Surveying Report	26	12-Jan-25	10-Feb-25	12-Jan-25 A	02-Mar-25 A	0	0	100%	100%
Engineering Works		31	12-Jan-25	16-Feb-25	12-Jan-25 A	02-Jun-25 A	3,015,067	3,015,067	100%	100%
Design Reviews		9	12-Jan-25	21-Jan-25	12-Jan-25 A	21-Jan-25 A	0	0	0%	0%
Infrastructure Networks		9	12-Jan-25	21-Jan-25	12-Jan-25 A	21-Jan-25 A	0	0	0%	0%
Road Works		9	12-Jan-25	21-Jan-25	12-Jan-25 A	21-Jan-25 A	0	0	0%	0%
Sewage Network		9	12-Jan-25	21-Jan-25	12-Jan-25 A	21-Jan-25 A	0	0	0%	0%
Storm Drainage Network		9	12-Jan-25	21-Jan-25	12-Jan-25 A	21-Jan-25 A	0	0	0%	0%
Potable Water Network		9	12-Jan-25	21-Jan-25	12-Jan-25 A	21-Jan-25 A	0	0	0%	0%
Irrigation Network		9	12-Jan-25	21-Jan-25	12-Jan-25 A	21-Jan-25 A	0	0	0%	0%
Medium Voltage Network		9	12-Jan-25	21-Jan-25	12-Jan-25 A	21-Jan-25 A	0	0	0%	0%
Street Lighting Network		9	12-Jan-25	21-Jan-25	12-Jan-25 A	21-Jan-25 A	0	0	0%	0%
Telecom Network		9	12-Jan-25	21-Jan-25	12-Jan-25 A	21-Jan-25 A	0	0	0%	0%
Superstructure Works		9	12-Jan-25	21-Jan-25	12-Jan-25 A	21-Jan-25 A	0	0	0%	0%
Sewage Pump Stations (PS06)		9	12-Jan-25	21-Jan-25	12-Jan-25 A	21-Jan-25 A	0	0	0%	0%
Storm Drainage Ponds (PO-J1 , PO-J2)		9	12-Jan-25	21-Jan-25	12-Jan-25 A	21-Jan-25 A	0	0	0%	0%
Shop Drawings		17	22-Jan-25	10-Feb-25	22-Jan-25 A	19-May-25 A	0	0	0%	0%
Infrastructure Networks		17	22-Jan-25	10-Feb-25	22-Jan-25 A	19-May-25 A	0	0	0%	0%
Road Works		17	22-Jan-25	10-Feb-25	22-Jan-25 A	19-May-25 A	0	0	0%	0%
Sewage Network		12	22-Jan-25	04-Feb-25	22-Jan-25 A	28-Apr-25 A	0	0	0%	0%
Storm Drainage Network		16	22-Jan-25	09-Feb-25	22-Jan-25 A	09-Feb-25 A	0	0	0%	0%
Potable Water Network		15	22-Jan-25	08-Feb-25	22-Jan-25 A	13-May-25 A	0	0	0%	0%
Irrigation Network		16	22-Jan-25	09-Feb-25	22-Jan-25 A	28-Apr-25 A	0	0	0%	0%
Medium Voltage Network		16	22-Jan-25	09-Feb-25	22-Jan-25 A	09-Feb-25 A	0	0	0%	0%
Street Lighting Network		16	22-Jan-25	09-Feb-25	22-Jan-25 A	09-Feb-25 A	0	0	0%	0%
Telecom Network		16	22-Jan-25	09-Feb-25	22-Jan-25 A	09-Feb-25 A	0	0	0%	0%
Superstructure Works		17	22-Jan-25	10-Feb-25	22-Jan-25 A	10-Feb-25 A	0	0	0%	0%
Sewage Pump Stations (PS 06)		17	22-Jan-25	10-Feb-25	22-Jan-25 A	10-Feb-25 A	0	0	0%	0%
Storm Drainage Ponds (PO-J1 , PO-J2)		17	22-Jan-25	10-Feb-25	22-Jan-25 A	10-Feb-25 A	0	0	0%	0%
Method Statements		17	22-Jan-25	10-Feb-25	22-Jan-25 A	10-Feb-25 A	0	0	0%	0%
Infrastructure Networks		17	22-Jan-25	10-Feb-25	22-Jan-25 A	10-Feb-25 A	0	0	0%	0%
Road Works		17	22-Jan-25	10-Feb-25	22-Jan-25 A	10-Feb-25 A	0	0	0%	0%
Sewage Network		12	22-Jan-25	04-Feb-25	22-Jan-25 A	08-Feb-25 A	0	0	0%	0%
Storm Drainage Network		16	22-Jan-25	09-Feb-25	22-Jan-25 A	09-Feb-25 A	0	0	0%	0%
Potable Water Network		15	22-Jan-25	08-Feb-25	22-Jan-25 A	08-Feb-25 A	0	0	0%	0%
Irrigation Network		16	22-Jan-25	09-Feb-25	22-Jan-25 A	09-Feb-25 A	0	0	0%	0%
Medium Voltage Network		16	22-Jan-25	09-Feb-25	22-Jan-25 A	09-Feb-25 A	0	0	0%	0%

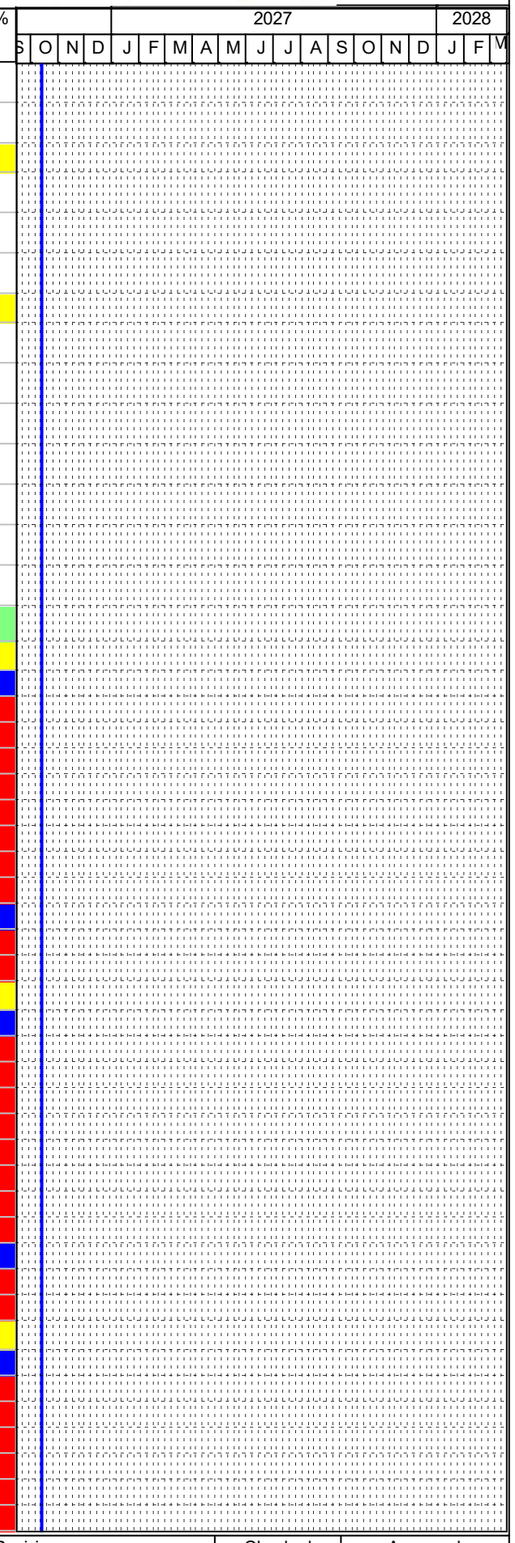

Primary Baseline
Remaining Work
Critical Remaining Work
Actual Work
Baseline Milestone
Milestone
Summary

Date	Revision	Checked	Approved
13-Oct-26	Third Industrial City		

Activity ID	Activity Name	Original Duration	BL Project Start	BL Project Finish	Start	Finish	BL Project Total Cost	Earned Value Cost	Schedule % Complete	Performance % Complete
	Street Lighting Network	16	22-Jan-25	09-Feb-25	22-Jan-25 A	09-Feb-25 A	0	0	0%	0%
	Telecom Network	16	22-Jan-25	09-Feb-25	22-Jan-25 A	09-Feb-25 A	0	0	0%	0%
	Superstructure Works	17	22-Jan-25	10-Feb-25	22-Jan-25 A	10-Feb-25 A	0	0	0%	0%
	Sewage Pump Stations (PS 06)	17	22-Jan-25	10-Feb-25	22-Jan-25 A	10-Feb-25 A	0	0	0%	0%
	Storm Drainage Ponds (PO-J1 , PO-J2)	17	22-Jan-25	10-Feb-25	22-Jan-25 A	10-Feb-25 A	0	0	0%	0%
	Material Submittals	22	22-Jan-25	16-Feb-25	22-Jan-25 A	02-Jun-25 A	3,015,067	3,015,067	100%	100%
	Short Lead Time Items	22	22-Jan-25	16-Feb-25	22-Jan-25 A	01-Jun-25 A	2,848,901	2,848,901	100%	100%
	Infrastructure Networks	22	22-Jan-25	16-Feb-25	22-Jan-25 A	01-Jun-25 A	2,736,286	2,736,286	100%	100%
	Superstructure Works	17	22-Jan-25	10-Feb-25	22-Jan-25 A	11-May-25 A	112,614	112,614	100%	100%
	Long Lead Time Items	17	22-Jan-25	10-Feb-25	01-Feb-25 A	02-Jun-25 A	166,166	166,166	100%	100%
	Infrastructure Networks	7	22-Jan-25	30-Jan-25	01-Feb-25 A	23-May-25 A	30,059	30,059	100%	100%
	Superstructure Works	17	22-Jan-25	10-Feb-25	11-May-25 A	02-Jun-25 A	136,108	136,108	100%	100%
	Procurement Cycle	749	05-Feb-25	05-Oct-26	11-Feb-25 A	29-Jul-27	20,007,776	17,515,838	100%	87.55%
	Short Lead Time Items	749	05-Feb-25	05-Oct-26	11-Feb-25 A	29-Jul-27	18,900,000	17,029,604	100%	90.1%
	Infrastructure Networks	749	05-Feb-25	05-Oct-26	11-Feb-25 A	29-Jul-27	17,093,229	15,250,911	100%	89.22%
	Road Works	744	11-Feb-25	05-Oct-26	11-Feb-25 A	29-Jul-27	4,749,285	3,417,253	100%	71.95%
	Sewage Network	665	05-Feb-25	29-Mar-26	11-Feb-25 A	17-Apr-27	2,490,411	2,490,411	100%	100%
	Storm Drainage Network	670	11-Feb-25	29-Mar-26	11-Feb-25 A	28-Apr-27	4,387,027	4,387,027	100%	100%
	Potable Water Network	662	09-Feb-25	09-Feb-26	11-Feb-25 A	17-Apr-27	2,044,188	1,749,461	100%	85.58%
	Irrigation Network	574	11-Feb-25	21-Dec-25	11-Feb-25 A	02-Jan-27	1,248,318	1,223,846	100%	98.04%
	Medium Voltage Network	732	11-Feb-25	04-Mar-26	11-Feb-25 A	11-Jan-27	885,929	849,995	100%	95.94%
	Street Lighting Network	744	11-Feb-25	23-Jun-26	11-Feb-25 A	29-Jul-27	924,756	769,602	100%	83.22%
	Telecom Network	280	11-Feb-25	14-Jan-26	11-Feb-25 A	16-Aug-26 A	363,314	363,314	100%	100%
	Superstructure Works	584	18-Feb-25	14-Feb-26	18-Feb-25 A	20-Jan-27	1,806,771	1,778,694	100%	98.45%
	Issuance of Purchase Orders	24	18-Feb-25	18-Mar-25	18-Feb-25 A	30-Mar-25 A	0	0	0%	0%
	Manufacturing of Material	546	05-Mar-25	25-Oct-25	07-Mar-25 A	21-Dec-26	0	0	0%	0%
	1st Material Delivery & Site Inspection	440	13-Aug-25	24-Nov-25	04-Oct-25 A	20-Jan-27	0	0	0%	0%
	Material Delivery & Site Inspection	130	15-Sep-25	14-Feb-26	29-Oct-25 A	20-Jan-27	1,806,771	1,778,694	100%	98.45%
	Long Lead Time Items	629	10-Feb-25	31-Aug-26	11-Feb-25 A	09-Dec-26	1,107,776	486,234	100%	43.89%
	Infrastructure Networks	300	10-Feb-25	05-Feb-26	11-Feb-25 A	20-Sep-26 A	71,872	71,872	100%	100%
	RMU Works of Medium Voltage Network	300	10-Feb-25	05-Feb-26	11-Feb-25 A	20-Sep-26 A	71,872	71,872	100%	100%
	Superstructure Works	449	18-Sep-25	31-Aug-26	01-Jun-25 A	09-Dec-26	1,035,904	414,362	100%	40%
	Sewage Pump Stations (PS 06)	449	18-Sep-25	31-Aug-26	01-Jun-25 A	09-Dec-26	1,035,904	414,362	100%	40%
	Construction Works	856	09-Feb-25	28-Dec-26	11-Feb-25 A	06-Dec-27	82,973,345	60,167,489	91.47%	72.51%
	Infrastructure Networks	856	09-Feb-25	28-Dec-26	11-Feb-25 A	06-Dec-27	76,594,730	58,484,429	91.52%	76.36%
	Phase 2 Block "J"	769	09-Feb-25	01-Dec-26	11-Feb-25 A	15-Sep-27	63,588,438	53,415,159	98.1%	84%
	Rising Main Network	388	01-Sep-25	13-Nov-25	27-Dec-25 A	05-Nov-26	3,537,626	3,038,902	100%	85.9%
	Road 09 Local 2 (2278 LM)	669	16-Jun-25	01-Oct-26	26-Mar-25 A	11-Sep-27	21,436,707	17,217,181	100%	80.32%
	Road 10 Local 2 (2352 LM)	603	19-May-25	01-Oct-26	15-Mar-25 A	11-Jul-27	16,016,074	11,847,780	100%	73.97%
	Road 11 Local 1 (670 LM)	581	04-Aug-25	13-Oct-26	23-Apr-25 A	02-Aug-27	5,429,772	5,129,610	99.88%	94.47%
	Road 14 Local 1 (584 LM)	621	09-Jul-25	27-Oct-26	17-Apr-25 A	16-Aug-27	6,260,663	5,574,444	97.17%	89.04%
	Road 15 Local 1 (556 LM)	559	26-Apr-25	08-Nov-26	13-Apr-25 A	01-Sep-27	3,105,315	2,999,148	94.05%	96.58%
	Road 16 Local 1 (527 LM)	499	29-Mar-25	19-Nov-26	13-Mar-25 A	15-Sep-27	2,501,958	2,461,587	83.5%	98.39%
	Road 17 Local 1 (500 LM)	547	05-Mar-25	01-Dec-26	27-Feb-25 A	22-Dec-26	2,639,651	2,537,493	83.87%	96.13%
	Road 18 Local 1 (479 LM)	541	09-Feb-25	01-Jan-26	11-Feb-25 A	22-Nov-26	2,660,672	2,609,013	100%	98.06%
	Finishes for Infrastructure Networks	426	04-May-26	28-Dec-26	20-Sep-25 A	06-Dec-27	13,006,292	5,069,270	59.37%	38.98%
	Phase 2 Block "J"	426	04-May-26	28-Dec-26	20-Sep-25 A	06-Dec-27	13,006,292	5,069,270	59.37%	38.98%
	Independent Works	569	21-Jan-26	28-Dec-26	19-May-25 A	06-Dec-27	6,378,615	1,683,060	90.77%	26.39%
	Tie In To Existing Networks	215	02-Sep-26	28-Dec-26	24-Mar-27	06-Dec-27	0	0	0%	0%
	Phase 2 Block "J"	215	02-Sep-26	28-Dec-26	24-Mar-27	06-Dec-27	0	0	0%	0%
	Sewage Pump Stations	376	15-Mar-26	01-Dec-26	01-Sep-26 A	15-Jun-27	4,389,808	9,568	86.6%	0.22%
	Sewage Pump Station (PS 06)	376	15-Mar-26	01-Dec-26	01-Sep-26 A	15-Jun-27	4,389,808	9,568	86.6%	0.22%
	Storm Drainage Ponds	462	21-Jan-26	24-Aug-26	19-May-25 A	02-Aug-27	1,988,807	1,673,493	100%	84.15%
	Storm Drainage Pond (PO-J1)	355	21-Jan-26	30-Jul-26	19-May-25 A	24-Mar-27	1,702,195	1,673,493	100%	98.31%
	Storm Drainage Pond (PO-J2)	157	15-Feb-26	24-Aug-26	21-Jan-27	02-Aug-27	286,611	0	100%	0%

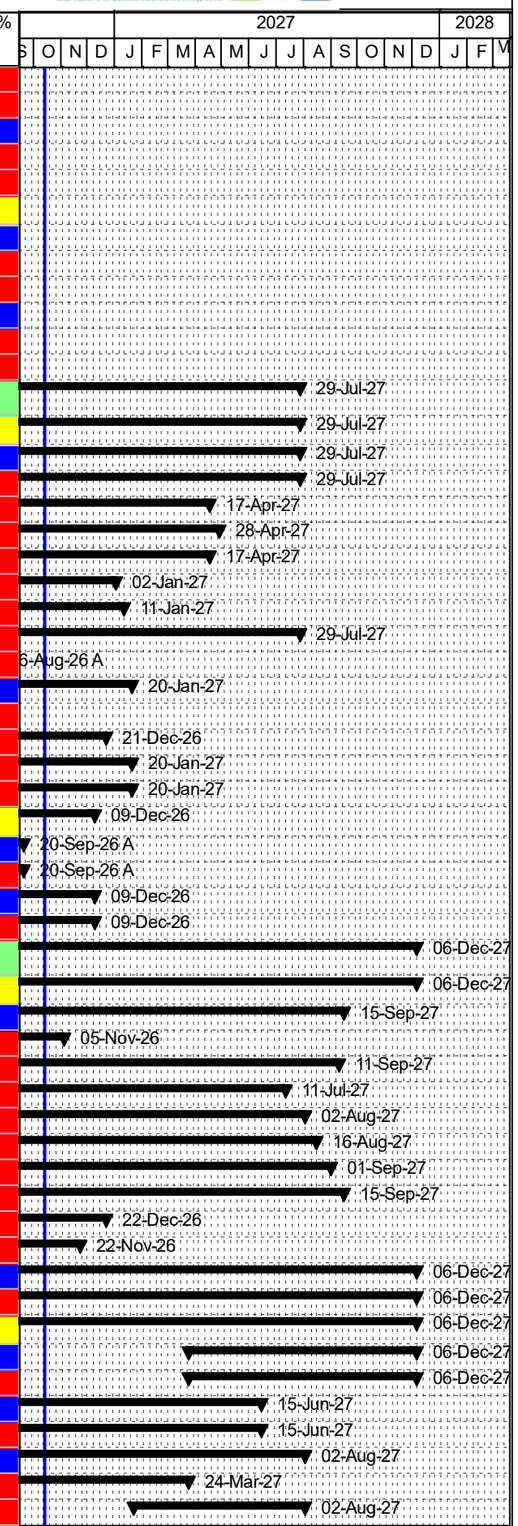


Primary Baseline | Actual Work | Summary
Remaining Work | Baseline Milestone
Critical Remaining Work | Milestone

Date	Revision	Checked	Approved
13-Oct-26	Third Industrial City		

Infrastructure Works of Area J -3rd Industrial City-
Dammam-Phase 2 - Update 13-10-2026
WPR UPS LEVEL 5


Activity ID	Activity Name	Original Duration	BL Project Start	BL Project Finish	Start	Finish	BL Project Total Cost	Earned Value Cost	Schedule % Complete	Performance % Complete
Testing and Comissioning		278	25-Aug-26	03-Jan-27	01-Jun-26 A	06-Dec-27	11,395,586	7,359,977	2.6%	64.59%
Infrastructure Networks		50	07-Nov-26	03-Jan-27	01-Jun-26 A	06-Dec-27	11,075,669	7,359,977	0%	66.45%
Irrigation Network		12	12-Nov-26	25-Nov-26	05-Jun-26 A	05-Aug-27	624,274	156,068	0%	25%
T/C-IR	Testing and Commissioning of Irrigation Network	12	12-Nov-26	25-Nov-26	05-Jun-26 A	05-Aug-27	624,274	156,068	0%	25%
Potable Water Network		12	03-Dec-26	16-Dec-26	01-Jul-26 A	18-Oct-27	1,022,094	613,257	0%	60%
T/C-PW	Testing and Commissioning of Potable Water Network	12	03-Dec-26	16-Dec-26	01-Jul-26 A	18-Oct-27	1,022,094	613,257	0%	60%
Sewage Network		12	19-Dec-26	31-Dec-26	01-Jun-26 A	07-Oct-27	2,308,897	1,962,563	0%	85%
T/C-SW	Testing and Commissioning of Sewage Network	12	19-Dec-26	31-Dec-26	01-Jun-26 A	07-Oct-27	2,308,897	1,962,563	0%	85%
Storm Drainage Network		10	21-Dec-26	31-Dec-26	10-Jun-26 A	09-Sep-27	2,866,651	2,436,654	0%	85%
T/C-SD	Testing and Commissioning of Storm Drainage Network	10	21-Dec-26	31-Dec-26	10-Jun-26 A	09-Sep-27	2,866,651	2,436,654	0%	85%
Street Lighting Network		18	07-Nov-26	26-Nov-26	05-Sep-26 A	24-Oct-27	462,378	147,961	0%	32%
T/C-SL	Testing and Commissioning of Street Lighting Network	18	07-Nov-26	26-Nov-26	05-Sep-26 A	24-Oct-27	462,378	147,961	0%	32%
Telecom Network		10	10-Nov-26	21-Nov-26	05-Sep-26 A	06-Sep-27	181,657	58,130	0%	32%
T/C-TE	Testing and Commissioning of Telecom Network	10	10-Nov-26	21-Nov-26	05-Sep-26 A	06-Sep-27	181,657	58,130	0%	32%
Medium Voltage Network		10	22-Nov-26	02-Dec-26	05-Sep-26 A	06-Sep-27	478,905	263,398	0%	55%
T/C-MV	Testing and Commissioning of Medium Voltage Network	10	22-Nov-26	02-Dec-26	05-Sep-26 A	06-Sep-27	478,905	263,398	0%	55%
Road Works		5	29-Dec-26	03-Jan-27	16-Aug-26 A	06-Dec-27	3,130,812	1,721,947	0%	55%
T/C-RD	Testing and Commissioning of Road Works	5	29-Dec-26	03-Jan-27	16-Aug-26 A	06-Dec-27	3,130,812	1,721,947	0%	55%
Independent Works		56	25-Aug-26	31-Dec-26	03-Aug-27	07-Oct-27	319,918	0	92.79%	0%
T/C-SPS	Testing and Commissioning of Sewage Pump Stations	26	02-Dec-26	31-Dec-26	07-Sep-27	07-Oct-27	23,081	0	0%	0%
T/C-DPO	Testing and Commissioning of Storm Drainage Ponds	30	25-Aug-26	29-Sep-26	03-Aug-27	06-Sep-27	296,837	0	100%	0%
Handing over and close out		160	17-Oct-26	11-Jan-27	16-Jun-27	20-Dec-27	0	0	0%	0%
As-Built		155	17-Oct-26	05-Jan-27	16-Jun-27	14-Dec-27	0	0	0%	0%
HO-190	As-Built Drawing For Potable Water Network	12	19-Nov-26	02-Dec-26	05-Oct-27	18-Oct-27	0	0	0%	0%
HO-180	Submission As-Built Drawing For Irrigation Network	12	29-Oct-26	11-Nov-26	24-Jul-27	05-Aug-27	0	0	0%	0%
HO-170	Submission As-Built Drawing For Medium Voltage Network	12	12-Nov-26	25-Nov-26	07-Aug-27	19-Aug-27	0	0	0%	0%
HO-130	Submission As-Built Drawing For Pond	12	12-Nov-26	25-Nov-26	07-Aug-27	19-Aug-27	0	0	0%	0%
HO-210	Submission As-Built Drawing For Pump station	12	02-Dec-26	15-Dec-26	16-Jun-27	29-Jun-27	0	0	0%	0%
HO-140	Submission As-Built Drawing For Roads Network	5	29-Dec-26	03-Jan-27	06-Dec-27	12-Dec-27	0	0	0%	0%
HO-100	Submission As-Built Drawing For Sewage Network	7	29-Dec-26	05-Jan-27	06-Dec-27	14-Dec-27	0	0	0%	0%
HO-200	Submission As-Built Drawing For Storm Network	12	13-Dec-26	26-Dec-26	02-Sep-27	15-Sep-27	0	0	0%	0%
HO-150	Submission As-Built Drawing For Street Lighting Network	12	17-Oct-26	29-Oct-26	04-Oct-27	17-Oct-27	0	0	0%	0%
HO-160	Submission As-Built Drawing For Telecom Network	12	12-Nov-26	25-Nov-26	07-Aug-27	19-Aug-27	0	0	0%	0%
De-Mobilization Works		5	04-Jan-27	09-Jan-27	08-Dec-27	14-Dec-27	0	0	0%	0%
HO-120	Remove material stock & Storage area	5	04-Jan-27	09-Jan-27	08-Dec-27	14-Dec-27	0	0	0%	0%
HO-230	Remove Temporary Car Shades	5	04-Jan-27	09-Jan-27	08-Dec-27	14-Dec-27	0	0	0%	0%
HO-220	Removing Portable Caravan	5	04-Jan-27	09-Jan-27	08-Dec-27	14-Dec-27	0	0	0%	0%
Handing Over		10	04-Jan-27	11-Jan-27	08-Dec-27	20-Dec-27	0	0	0%	0%
HO-110	Final Testing Work	5	04-Jan-27	09-Jan-27	08-Dec-27	14-Dec-27	0	0	0%	0%
HO-240	Final Walkthrough and Inspection	2	10-Jan-27	11-Jan-27	18-Dec-27	20-Dec-27	0	0	0%	0%

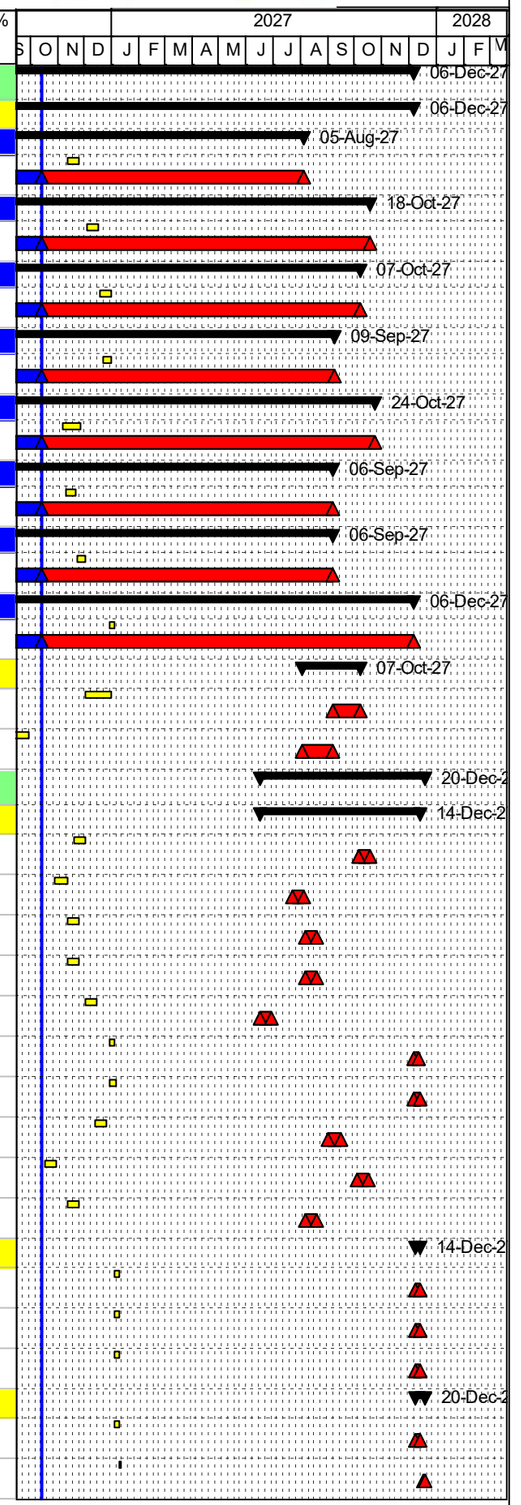

Primary Baseline · Remaining Work · Critical Remaining Work · Actual Work · Baseline Milestone · Milestone · Summary

Date	Revision	Checked	Approved
13-Oct-26	Third Industrial City		

Activity ID	Activity Name	Original Duration	BL Project Start	BL Project Finish	Start	Finish	BL Project Total Cost	Earned Value Cost	Schedule % Complete	Performance % Complete
HO-280	Punch List Completion	2	10-Jan-27	11-Jan-27	18-Dec-27	20-Dec-27	0	0	0%	0%
HO-250	Review B.O.Q Qty. to ensure compliance with the actual status	5	04-Jan-27	09-Jan-27	12-Dec-27	18-Dec-27	0	0	0%	0%
HO-260	Review FIR Approval to ensure compliance with the actual status	5	04-Jan-27	09-Jan-27	12-Dec-27	18-Dec-27	0	0	0%	0%
HO-270	Review the sample drawing to ensure compliance with the actual status	5	04-Jan-27	09-Jan-27	12-Dec-27	18-Dec-27	0	0	0%	0%



Primary Baseline
Remaining Work
Critical Remaining Work
Actual Work
Baseline Milestone
Milestone
Summary

Date	Revision	Checked	Approved
13-Oct-26	Third Industrial City		
