
Infrastructure Works of Area J -3rd Industrial City-Dammam-Phase 2 - Update 13-10-2026

3Week Lookahead Schedule

Activity ID	Activity Name	Original Duration	Start	Finish	BL Project Start	BL Project Finish	Budgeted Total Cost
Infrastructure Works of Area J -3rd Industrial City-Dammam-Phase 2 - Upd		499	29-Oct-25 A	06-Dec-27	19-Mar-25	03-Jan-27	25,622,598
Procurement Cycle		432	29-Oct-25 A	24-Apr-27	03-May-25	31-Aug-26	3,586,800
Short Lead Time Items		432	29-Oct-25 A	24-Apr-27	03-May-25	05-Jul-26	2,550,896
Infrastructure Networks		424	13-Dec-25 A	24-Apr-27	03-May-25	05-Jul-26	1,957,222
Road Works		32	13-Oct-26	18-Nov-26	20-Jul-25	05-Jul-26	1,232,660
1st Material Delivery & Site Inspection		6	13-Oct-26	19-Oct-26	20-Jul-25	18-Aug-25	0
Pavement Works		6	13-Oct-26	19-Oct-26	20-Jul-25	26-Jul-25	0
PRO-RD-1DL-140	1ST Material Delivery for Interlock Tiles of Landscaping	6	13-Oct-26	19-Oct-26	20-Jul-25	26-Jul-25	0
PRO-RD-1DL-150	1ST Material Delivery for Curbstones of Landscaping	6	13-Oct-26	19-Oct-26	20-Jul-25	26-Jul-25	0
Traffic Signs Boards and Roads Marking		6	13-Oct-26	19-Oct-26	12-Aug-25	18-Aug-25	0
PRO-RD-1DL-160	1ST Material Delivery for Traffic Signs Boards of Road Works	6	13-Oct-26	19-Oct-26	12-Aug-25	18-Aug-25	0
PRO-RD-1DL-170	1ST Material Delivery for Road Markings of Road Works	6	13-Oct-26	19-Oct-26	12-Aug-25	18-Aug-25	0
Material Delivery & Site Inspection		32	13-Oct-26	18-Nov-26	28-Dec-25	05-Jul-26	1,232,660
Road 18 Local 1 (479 LM)		26	20-Oct-26	18-Nov-26	28-Dec-25	26-Jan-26	1,971
Traffic Signs Boards and Roads Marking		26	20-Oct-26	18-Nov-26	28-Dec-25	26-Jan-26	1,971
PRO-R18-RD-DL	Material Delivery & Site Inspection of Traffic Signs Boards For Road Works	26	20-Oct-26	18-Nov-26	28-Dec-25	26-Jan-26	1,971
Road 10 Local 2 (2352 LM)		26	13-Oct-26	11-Nov-26	26-Feb-26	30-Apr-26	616,209
Bituminous Construction		26	13-Oct-26	11-Nov-26	26-Feb-26	30-Apr-26	616,209
PRO-R10-RD-DL	Material Delivery & Site Inspection for Prime Coat of Road Works	26	13-Oct-26	11-Nov-26	26-Feb-26	31-Mar-26	123,243
PRO-R10-RD-DL	Material Delivery & Site Inspection for Bituminous Base & Wearing Courses of Road	26	13-Oct-26	11-Nov-26	01-Apr-26	30-Apr-26	492,966
Road 09 Local 2 (2278 LM)		26	13-Oct-26	11-Nov-26	02-May-26	05-Jul-26	614,480
Bituminous Construction		26	13-Oct-26	11-Nov-26	02-May-26	05-Jul-26	614,480
PRO-R09-RD-DL	Material Delivery & Site Inspection for Prime Coat of Road Works	26	13-Oct-26	11-Nov-26	02-May-26	04-Jun-26	122,896
PRO-R09-RD-DL	Material Delivery & Site Inspection for Bituminous Base & Wearing Courses of Road	26	13-Oct-26	11-Nov-26	06-Jun-26	05-Jul-26	491,584
Sewage Network		38	13-Oct-26	25-Nov-26	26-Jul-25	25-Oct-25	0
Material Delivery & Site Inspection		38	13-Oct-26	25-Nov-26	26-Jul-25	25-Oct-25	0
Road 17 Local 1 (500 LM)		26	13-Oct-26	11-Nov-26	25-Aug-25	25-Oct-25	0
Testing and Finishes		26	13-Oct-26	11-Nov-26	25-Aug-25	25-Oct-25	0
PRO-R17-SW-DL	Material Delivery & Site Inspection of Manholes Covers for Sewage Network	26	13-Oct-26	11-Nov-26	25-Aug-25	24-Sep-25	0
PRO-R17-SW-DL	Material Delivery & Site Inspection of Membrane Insulation for Sewage Network	26	13-Oct-26	11-Nov-26	25-Sep-25	25-Oct-25	0
Road 09 Local 2 (2278 LM)		38	13-Oct-26	25-Nov-26	26-Jul-25	07-Sep-25	0
Testing and Finishes		38	13-Oct-26	25-Nov-26	26-Jul-25	07-Sep-25	0
PRO-R09-SW-DL	Material Delivery & Site Inspection of Manholes Covers for Rising Main Network	38	13-Oct-26	25-Nov-26	26-Jul-25	07-Sep-25	0
PRO-R09-SW-DL	Material Delivery & Site Inspection of Membrane Insulation for Rising Main Network	38	13-Oct-26	25-Nov-26	26-Jul-25	07-Sep-25	0
Storm Drainage Network		408	20-Jun-26 A	23-Nov-26	26-Jul-25	25-Oct-25	0
Material Delivery & Site Inspection		408	20-Jun-26 A	23-Nov-26	26-Jul-25	25-Oct-25	0
Road 18 Local 1 (479 LM)		26	27-Jun-26 A	24-Oct-26	26-Jul-25	24-Aug-25	0
Testing and Finishes		26	27-Jun-26 A	24-Oct-26	26-Jul-25	24-Aug-25	0
PRO-R18-SD-DL·	Material Delivery & Site Inspection of Manholes Covers for Storm Drainage Network	26	27-Jun-26 A	24-Oct-26	26-Jul-25	24-Aug-25	0
PRO-R18-SD-DL·	Material Delivery & Site Inspection of Catch Basin Covers for Storm Drainage Netwo	26	27-Jun-26 A	24-Oct-26	26-Jul-25	24-Aug-25	0
PRO-R18-SD-DL·	Material Delivery & Site Inspection of Epoxy Insulation for Storm Drainage Network	26	27-Jun-26 A	24-Oct-26	26-Jul-25	24-Aug-25	0
Road 17 Local 1 (500 LM)		26	20-Jun-26 A	24-Oct-26	25-Aug-25	24-Sep-25	0
Testing and Finishes		26	20-Jun-26 A	24-Oct-26	25-Aug-25	24-Sep-25	0
PRO-R17-SD-DL·	Material Delivery & Site Inspection of Manholes Covers for Storm Drainage Network	26	20-Jun-26 A	24-Oct-26	25-Aug-25	24-Sep-25	0
PRO-R17-SD-DL·	Material Delivery & Site Inspection of Catch Basin Covers for Storm Drainage Netwo	26	20-Jun-26 A	24-Oct-26	25-Aug-25	24-Sep-25	0
PRO-R17-SD-DL·	Material Delivery & Site Inspection of Epoxy Insulation for Storm Drainage Network	26	20-Jun-26 A	24-Oct-26	25-Aug-25	24-Sep-25	0
Road 16 Local 1 (527 LM)		26	25-Oct-26	23-Nov-26	25-Sep-25	25-Oct-25	0
Testing and Finishes		26	25-Oct-26	23-Nov-26	25-Sep-25	25-Oct-25	0
PRO-R16-SD-DL·	Material Delivery & Site Inspection of Manholes Covers for Storm Drainage Network	26	25-Oct-26	23-Nov-26	25-Sep-25	25-Oct-25	0
PRO-R16-SD-DL·	Material Delivery & Site Inspection of Catch Basin Covers for Storm Drainage Netwo	26	25-Oct-26	23-Nov-26	25-Sep-25	25-Oct-25	0
PRO-R16-SD-DL·	Material Delivery & Site Inspection of Epoxy Insulation for Storm Drainage Network	26	25-Oct-26	23-Nov-26	25-Sep-25	25-Oct-25	0
Potable Water Network		360	13-Dec-25 A	11-Jan-27	31-May-25	10-Jan-26	221,047
1st Material Delivery & Site Inspection		6	13-Oct-26	19-Oct-26	31-May-25	10-Jun-25	0

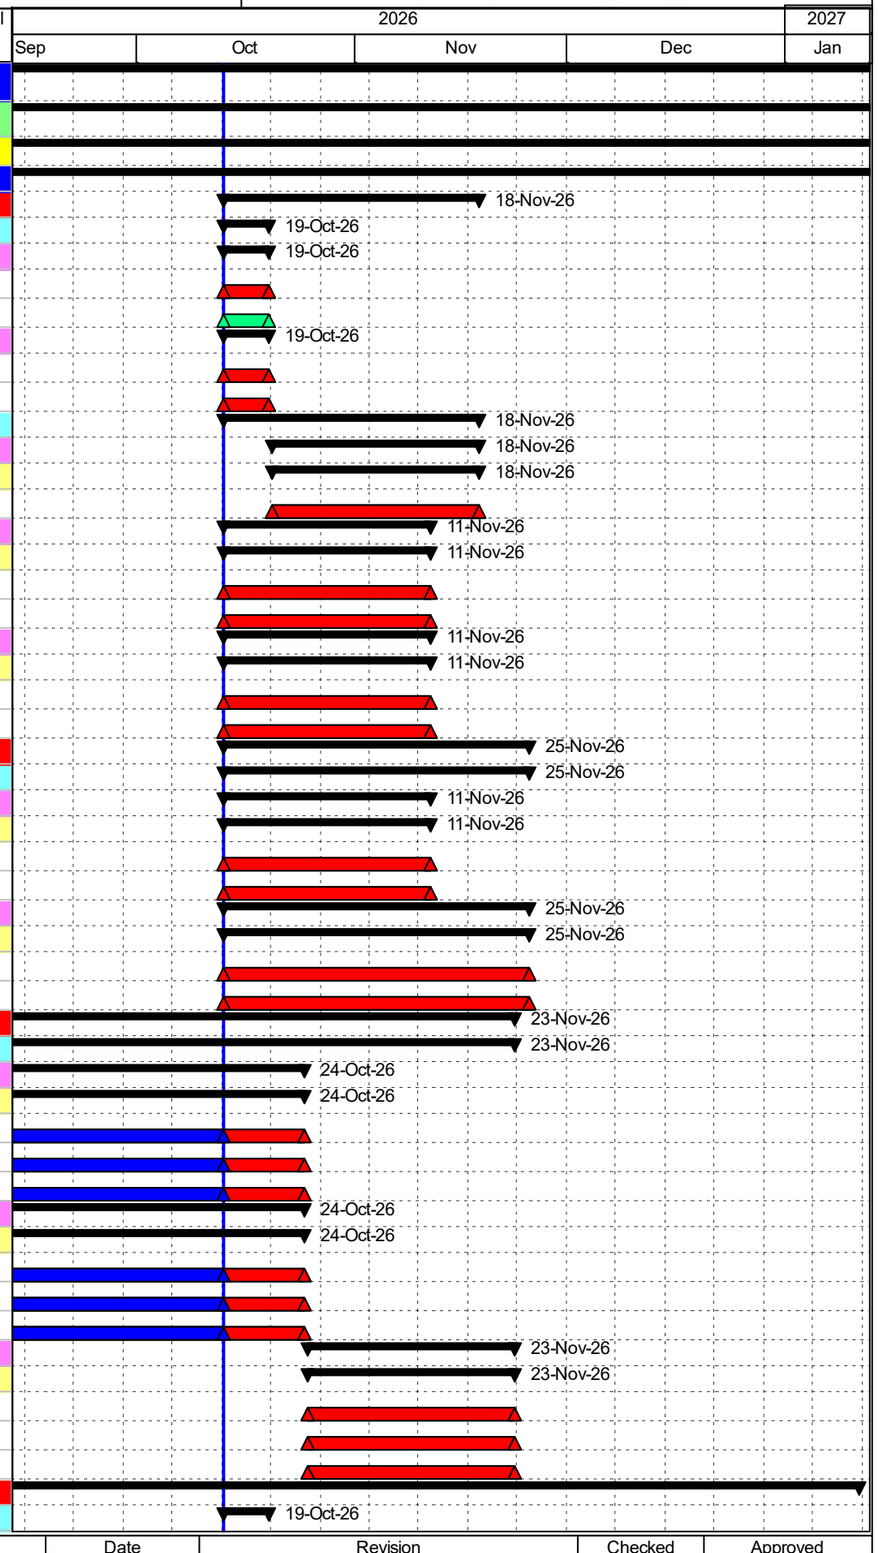


Primary Baseline · Actual Work · Summary · Remaining Work · Baseline Milestone · Critical Remaining Work · Milestone

Date	Revision	Checked	Approved
13-Oct-26	Third Industrial City		

Infrastructure Works of Area J -3rd Industrial City-
Dammam-Phase 2 - Update 13-10-2026
3Week Lookahead Schedule

Activity ID	Activity Name	Original Duration	Start	Finish	BL Project Start	BL Project Finish	Budgeted Total Cost
Testing and Finishes		6	13-Oct-26	19-Oct-26	31-May-25	10-Jun-25	0
PRO-PW-1DL-130	1ST Material Delivery for Finishes of Potable Water Network	6	13-Oct-26	19-Oct-26	31-May-25	10-Jun-25	0
Material Delivery & Site Inspection		360	13-Dec-25 A	11-Jan-27	11-Jun-25	10-Jan-26	221,047
Road 18 Local 1 (479 LM)		26	20-Oct-26	18-Nov-26	11-Jun-25	10-Jul-25	0
Testing and Finishes		26	20-Oct-26	18-Nov-26	11-Jun-25	10-Jul-25	0
PRO-R18-PW-DL	Material Delivery & Site Inspection for Finishes of Potable Water Network	26	20-Oct-26	18-Nov-26	11-Jun-25	10-Jul-25	0
Road 17 Local 1 (500 LM)		26	13-Oct-26	11-Nov-26	16-Jun-25	15-Jul-25	5,533
Main Line Sections		26	13-Oct-26	11-Nov-26	16-Jun-25	15-Jul-25	5,533
PRO-R17-PW-DL	Material Delivery & Site Inspection of Valves for Potable Water Network	26	13-Oct-26	11-Nov-26	16-Jun-25	15-Jul-25	5,533
Road 10 Local 2 (2352 LM)		26	13-Dec-25 A	11-Jan-27	15-Sep-25	15-Oct-25	215,514
Main Line Sections		26	13-Dec-25 A	11-Jan-27	15-Sep-25	15-Oct-25	215,514
PRO-R10-PW-DL	Material Delivery & Site Inspection of Valves for Potable Water Network	26	13-Dec-25 A	11-Jan-27	15-Sep-25	15-Oct-25	215,514
Road 09 Local 2 (2278 LM)		26	20-Oct-26	18-Nov-26	11-Dec-25	10-Jan-26	0
Testing and Finishes		26	20-Oct-26	18-Nov-26	11-Dec-25	10-Jan-26	0
PRO-R09-PW-DL	Material Delivery & Site Inspection for Finishes of Potable Water Network	26	20-Oct-26	18-Nov-26	11-Dec-25	10-Jan-26	0
Irrigation Network		22	13-Oct-26	07-Nov-26	17-Jul-25	11-Aug-25	4,632
1st Material Delivery & Site Inspection		6	13-Oct-26	19-Oct-26	17-Jul-25	23-Jul-25	0
Main Line Pipes		6	13-Oct-26	19-Oct-26	17-Jul-25	23-Jul-25	0
PRO-IR-1DL-110	1ST Material Delivery for Valves of Irrigation Network	6	13-Oct-26	19-Oct-26	17-Jul-25	23-Jul-25	0
Material Delivery & Site Inspection		16	20-Oct-26	07-Nov-26	24-Jul-25	11-Aug-25	4,632
Road 18 Local 1 (479 LM)		16	20-Oct-26	07-Nov-26	24-Jul-25	11-Aug-25	4,632
Main Line Pipes		16	20-Oct-26	07-Nov-26	24-Jul-25	11-Aug-25	4,632
PRO-R18-IR-DL-	Material Delivery & Site Inspection of Valves for Irrigation Network	16	20-Oct-26	07-Nov-26	24-Jul-25	11-Aug-25	4,632
Medium Voltage Network		324	13-Dec-25 A	12-Dec-26	03-May-25	20-Dec-25	359,338
1st Material Delivery & Site Inspection		52	13-Oct-26	12-Dec-26	03-May-25	10-Nov-25	0
RMU Concrete Works		52	13-Oct-26	12-Dec-26	10-Sep-25	10-Nov-25	0
PRO-MV-1DL-110	1ST Material Delivery for RMU Concrete Foundations of Medium Voltage Network	52	13-Oct-26	12-Dec-26	10-Sep-25	10-Nov-25	0
Termination and Testing Works		26	13-Oct-26	11-Nov-26	03-May-25	01-Jun-25	0
PRO-MV-1DL-120	1ST Material Delivery for Termination and Joints Kits of Medium Voltage Network	26	13-Oct-26	11-Nov-26	03-May-25	01-Jun-25	0
Material Delivery & Site Inspection		26	13-Dec-25 A	11-Nov-26	20-Nov-25	20-Dec-25	359,338
Road 09 Local 2 (2278 LM)		26	13-Dec-25 A	11-Nov-26	20-Nov-25	20-Dec-25	359,338
Cabling Works		26	13-Dec-25 A	11-Nov-26	20-Nov-25	20-Dec-25	359,338
PRO-R09-MV-DL-	Material Delivery & Site Inspection of Medium Voltage Cables for Medium Voltage N	26	13-Dec-25 A	11-Nov-26	20-Nov-25	20-Dec-25	359,338
Street Lighting Network		398	21-Sep-26 A	24-Apr-27	26-Jul-25	16-Mar-26	139,546
1st Material Delivery & Site Inspection		15	13-Oct-26	29-Oct-26	26-Jul-25	11-Aug-25	0
Lighting Poles Works		6	13-Oct-26	19-Oct-26	26-Jul-25	31-Jul-25	0
PRO-SL-1DL-140	1ST Material Delivery for Lighting Fixtures of Street Lighting Network	6	13-Oct-26	19-Oct-26	26-Jul-25	31-Jul-25	0
Distribution Panel Board		6	13-Oct-26	19-Oct-26	26-Jul-25	31-Jul-25	0
PRO-SL-1DL-160	1ST Material Delivery for Distrubution Panel Boards of Street Lighting Network	6	13-Oct-26	19-Oct-26	26-Jul-25	31-Jul-25	0
Termination and Testing Works		15	13-Oct-26	29-Oct-26	26-Jul-25	11-Aug-25	0
PRO-SL-1DL-130	1ST Material Delivery for Fuse Boxes of Street Lighting Network	15	13-Oct-26	29-Oct-26	26-Jul-25	11-Aug-25	0
PRO-SL-1DL-170	1ST Material Delivery for Cable Lugs of Street Lighting Network	15	13-Oct-26	29-Oct-26	26-Jul-25	11-Aug-25	0
Earthing System Works		6	13-Oct-26	19-Oct-26	26-Jul-25	31-Jul-25	0
PRO-SL-1DL-150	1ST Material Delivery for Lighting Earthing of Street Lighting Network	6	13-Oct-26	19-Oct-26	26-Jul-25	31-Jul-25	0
Material Delivery & Site Inspection		398	21-Sep-26 A	24-Apr-27	02-Aug-25	16-Mar-26	139,546
Road 18 Local 1 (479 LM)		26	20-Oct-26	18-Nov-26	16-Aug-25	14-Sep-25	3,755
Lighting Poles Works		26	20-Oct-26	18-Nov-26	16-Aug-25	14-Sep-25	3,755
PRO-R18-SL-DL-	Material Delivery & Site Inspection of Lighting Fixtures for Street Lighting Network	26	20-Oct-26	18-Nov-26	16-Aug-25	14-Sep-25	3,755
Road 10 Local 2 (2352 LM)		398	21-Sep-26 A	24-Apr-27	02-Aug-25	16-Mar-26	132,273
Distribution Panel Board		26	21-Sep-26 A	11-Nov-26	02-Aug-25	31-Aug-25	103,537
PRO-R10-SL-DL-	Material Delivery & Site Inspection of Distrubution Panel Boards for Street Lighting N	26	21-Sep-26 A	11-Nov-26	02-Aug-25	31-Aug-25	103,537
Termination and Testing Works		52	21-Sep-26 A	24-Apr-27	15-Jan-26	16-Mar-26	25,218
PRO-R10-SL-DL-	Material Delivery & Site Inspection of Fuse Boxes for Street Lighting Network	26	21-Sep-26 A	24-Mar-27	15-Jan-26	14-Feb-26	25,218
PRO-R10-SL-DL-	Material Delivery & Site Inspection of Cable Lugs for Street Lighting Network	26	21-Sep-26 A	24-Apr-27	15-Feb-26	16-Mar-26	0

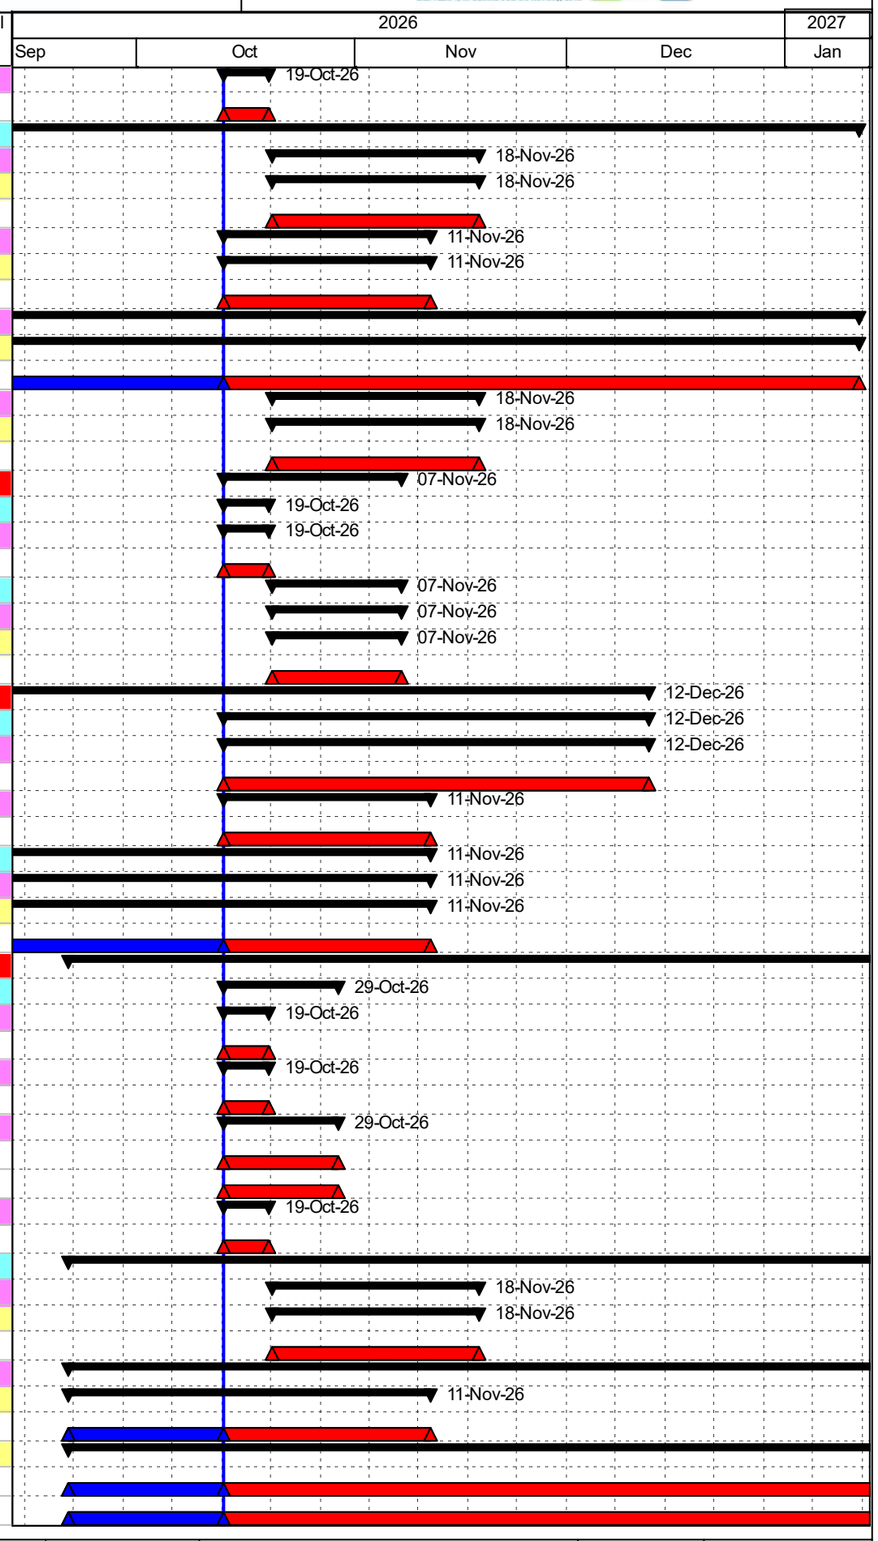


Primary Baseline
Remaining Work
Critical Remaining Work
Actual Work
Baseline Milestone
Milestone
Summary

Date	Revision	Checked	Approved
13-Oct-26	Third Industrial City		

Infrastructure Works of Area J -3rd Industrial City-
Dammam-Phase 2 - Update 13-10-2026
3Week Lookahead Schedule

Activity ID	Activity Name	Original Duration	Start	Finish	BL Project Start	BL Project Finish	Budgeted Total Cost
Earthing System Works		26	20-Oct-26	18-Nov-26	02-Aug-25	31-Aug-25	3,518
PRO-R10-SL-DL-	Material Delivery & Site Inspection of Lighting Earthing for Street Lighting Network	26	20-Oct-26	18-Nov-26	02-Aug-25	31-Aug-25	3,518
Road 09 Local 2 (2278 LM)		26	20-Oct-26	18-Nov-26	02-Aug-25	31-Aug-25	3,518
Earthing System Works		26	20-Oct-26	18-Nov-26	02-Aug-25	31-Aug-25	3,518
PRO-R09-SL-DL-	Material Delivery & Site Inspection of Lighting Earthing for Street Lighting Network	26	20-Oct-26	18-Nov-26	02-Aug-25	31-Aug-25	3,518
Superstructure Works		388	29-Oct-25 A	20-Jan-27	13-Aug-25	14-Feb-26	593,674
Manufacturing of Material		60	13-Oct-26	21-Dec-26	16-Aug-25	25-Oct-25	0
Storm Drainage Ponds (PO-J1 , PO-J2)		60	13-Oct-26	21-Dec-26	16-Aug-25	25-Oct-25	0
PRO-DPO-CV-MF-2	Manufacturing of Civil Works for Storm Drainage Ponds (PO-J2)	60	13-Oct-26	21-Dec-26	16-Aug-25	25-Oct-25	0
1st Material Delivery & Site Inspection		40	13-Oct-26	28-Nov-26	13-Aug-25	29-Sep-25	0
Sewage Pump Stations (PS 06)		40	13-Oct-26	28-Nov-26	13-Aug-25	29-Sep-25	0
PRO-SPS-CV-1DL-	1ST Material Delivery for Civil Works for Sewage Pump Stations (PS 06)	40	13-Oct-26	28-Nov-26	13-Aug-25	29-Sep-25	0
Material Delivery & Site Inspection		130	29-Oct-25 A	20-Jan-27	15-Sep-25	14-Feb-26	593,674
Storm Drainage Ponds (PO-J1 , PO-J2)		130	29-Oct-25 A	20-Jan-27	15-Sep-25	14-Feb-26	593,674
PRO-DPO-CV-DL-1	Material Delivery & Site Inspection for Civil Works for Storm Drainage Ponds (PO-J1	70	29-Oct-25 A	02-Jan-27	15-Sep-25	06-Dec-25	508,118
PRO-DPO-CV-DL-2	Material Delivery & Site Inspection for Civil Works for Storm Drainage Ponds (PO-J2	70	09-Sep-26 A	20-Jan-27	25-Nov-25	14-Feb-26	85,556
Long Lead Time Items		50	05-Oct-26 A	09-Dec-26	05-Jul-26	31-Aug-26	1,035,904
Superstructure Works		50	05-Oct-26 A	09-Dec-26	05-Jul-26	31-Aug-26	1,035,904
Sewage Pump Stations (PS 06)		50	05-Oct-26 A	09-Dec-26	05-Jul-26	31-Aug-26	1,035,904
Material Site Inspection		50	05-Oct-26 A	09-Dec-26	05-Jul-26	31-Aug-26	1,035,904
PRO-SPS7-LL-MSI-	Material Site Inspection for Electromechanical Works for Sewage Pump Stations (PS	50	05-Oct-26 A	09-Dec-26	05-Jul-26	31-Aug-26	1,035,904
Construction Works		499	10-Nov-25 A	15-Sep-27	19-Mar-25	19-Nov-26	10,960,130
Infrastructure Networks		499	10-Nov-25 A	15-Sep-27	19-Mar-25	19-Nov-26	10,887,416
Phase 2 Block "J"		499	10-Nov-25 A	15-Sep-27	19-Mar-25	19-Nov-26	9,090,460
Rising Main Network		367	17-Jan-26 A	05-Nov-26	27-Sep-25	13-Nov-25	2,786,828
Main Line Sections		42	25-Feb-26 A	05-Nov-26	27-Sep-25	13-Nov-25	1,336,086
CO-RM-SW-300	Pipes Laying Works for Main Lines of Rising Main Network	21	25-Feb-26 A	05-Nov-26	27-Sep-25	20-Oct-25	1,169,075
CO-RM-SW-310	Trench Backfilling and Compaction Works for Main Lines of Rising Main Network	21	01-Sep-26 A	05-Nov-26	21-Oct-25	13-Nov-25	167,011
Manholes		366	17-Jan-26 A	19-Oct-26	28-Sep-25	18-Oct-25	835,054
CO-RM-SW-330	Installation RC Footing Works for Main Line Manholes of Rising Main Network	3	17-Jan-26 A	15-Oct-26	28-Sep-25	30-Sep-25	66,804
CO-RM-SW-340	Install Grp Liner Wall Works for Main Line Manholes of Rising Main Network	6	17-Jan-26 A	19-Oct-26	01-Oct-25	07-Oct-25	501,032
CO-RM-SW-350	Pouring Grp Liner Wall Works for Main Line Manholes of Rising Main Network	3	18-Sep-26 A	15-Oct-26	08-Oct-25	11-Oct-25	66,804
CO-RM-SW-360	Backfilling Works for Main Line Manholes of Rising Main Network	5	21-Sep-26 A	18-Oct-26	12-Oct-25	16-Oct-25	100,206
CO-RM-SW-370	Testing Works for Main Line Manholes of Rising Main Network	1	01-Oct-26 A	13-Oct-26	18-Oct-25	18-Oct-25	100,206
Valves Chamber		329	14-May-26 A	01-Nov-26	05-Oct-25	01-Nov-25	615,689
CO-RM-SW-400	RC Wall Works for Valve Chambers and Washout chamber of Rising Main Network	7	14-May-26 A	13-Oct-26	05-Oct-25	12-Oct-25	389,454
CO-RM-SW-410	RC Slab Works for Valve Chambers and Washout chamber of Rising Main Network	7	13-Oct-26	20-Oct-26	13-Oct-25	20-Oct-25	43,273
CO-RM-SW-420	Insulation Works for Valve Chambers and Washout chamber of Rising Main Networl	2	21-Oct-26	22-Oct-26	21-Oct-25	22-Oct-25	43,273
CO-RM-SW-430	Backfilling Works for Valve Chambers and Washout chamber of Rising Main Network	5	24-Oct-26	28-Oct-26	23-Oct-25	28-Oct-25	53,143
CO-RM-SW-440	Testing and Covering Works for Valve Chambers and Washout chamber of Rising M	3	29-Oct-26	01-Nov-26	29-Oct-25	01-Nov-25	86,545
Road 09 Local 2 (2278 LM)		499	10-Nov-25 A	11-Sep-27	21-Jul-25	01-Oct-26	3,291,836
SW_1		426	02-May-26 A	11-Sep-27	11-Aug-25	24-Sep-26	2,090,899
Sewage Network		1	13-Oct-26	13-Oct-26	11-Aug-25	11-Aug-25	35,494
Manholes		1	13-Oct-26	13-Oct-26	11-Aug-25	11-Aug-25	35,494
CO-R09.S01-SW-	Testing Works for Main Line Manholes of Sewage Network-[Road 09] -[SW-1]	1	13-Oct-26	13-Oct-26	11-Aug-25	11-Aug-25	35,494
Storm Drainage Network		317	27-Jun-26 A	28-Oct-26	05-Oct-25	18-Nov-25	287,863
Manholes		2	07-Oct-26 A	14-Oct-26	05-Oct-25	06-Oct-25	38,389
CO-R09.S01-SD-	Testing Works for Manholes of Storm Drainage Network-[Road 09] -[SW-1]	2	07-Oct-26 A	14-Oct-26	05-Oct-25	06-Oct-25	38,389
Catch Basin Sections		317	27-Jun-26 A	28-Oct-26	15-Oct-25	18-Nov-25	249,475
CO-R09.S01-SD-	Trench Excavation and Bedding Works for Catch Basins of Storm Drainage Network-	6	27-Jun-26 A	19-Oct-26	15-Oct-25	21-Oct-25	41,579
CO-R09.S01-SD-	Installation and Pipes Laying Connection Works for Catch Basins of Storm Drainage	7	29-Jun-26 A	20-Oct-26	22-Oct-25	29-Oct-25	124,737
CO-R09.S01-SD-	Trench Backfilling and Compaction Works for Catch Basins of Storm Drainage Netwc	10	03-Aug-26 A	28-Oct-26	08-Nov-25	18-Nov-25	55,439
CO-R09.S01-SD-	Testing Works for Catch Basins of Storm Drainage Network-[Road 09] -[SW-1]	7	21-Oct-26	28-Oct-26	30-Oct-25	06-Nov-25	27,719

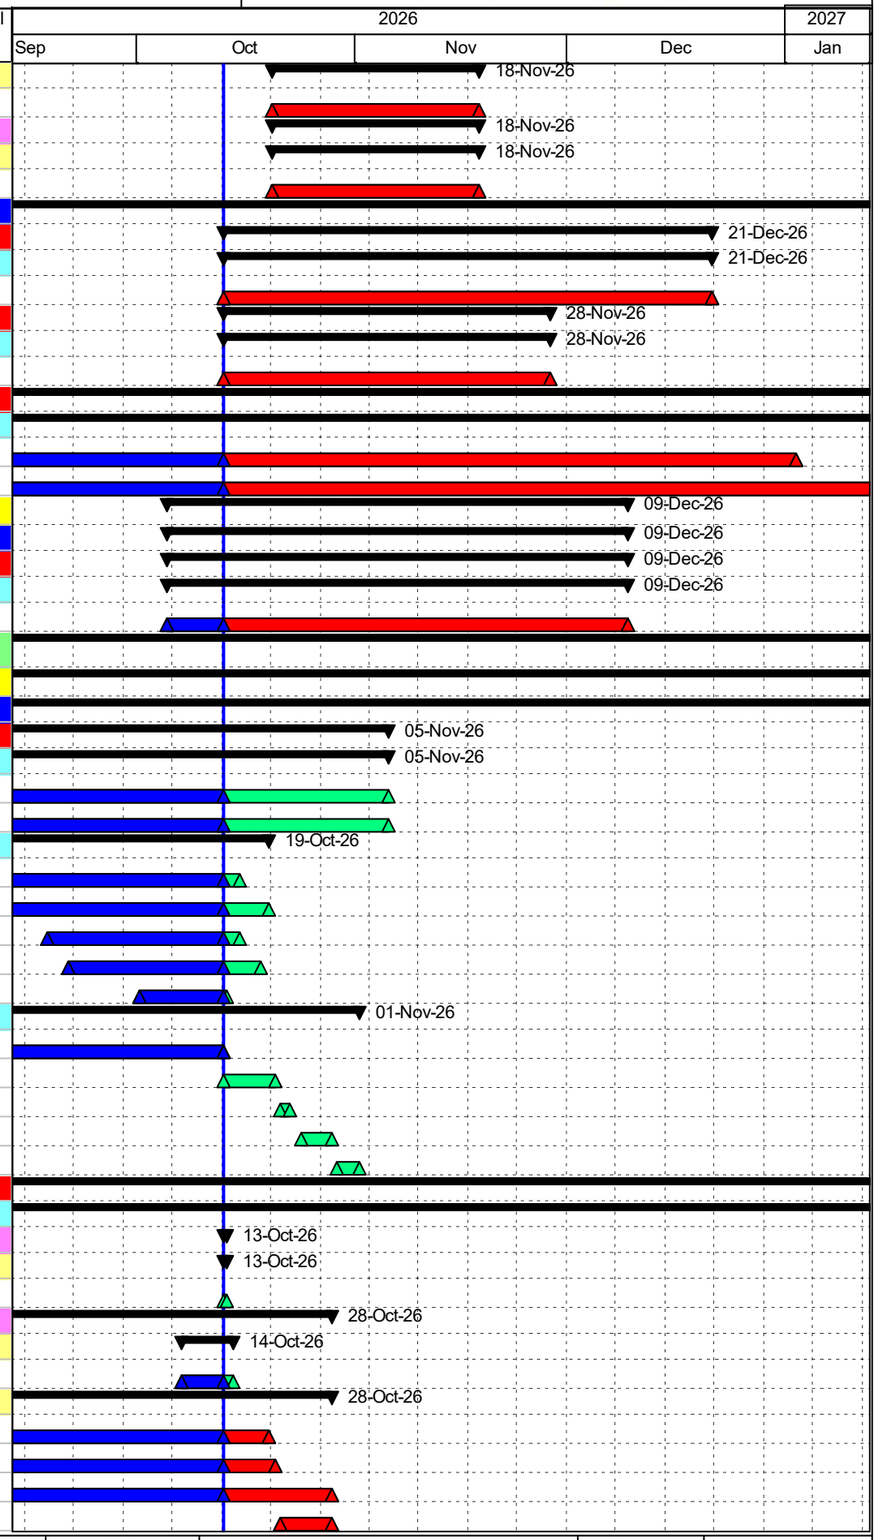


Primary Baseline
Remaining Work
Critical Remaining Work
Actual Work
Baseline Milestone
Milestone
Summary

Date	Revision	Checked	Approved
13-Oct-26	Third Industrial City		

Infrastructure Works of Area J -3rd Industrial City-
Dammam-Phase 2 - Update 13-10-2026
3Week Lookahead Schedule

Activity ID	Activity Name	Original Duration	Start	Finish	BL Project Start	BL Project Finish	Budgeted Total Cost
Irrigation Network		273	02-May-26 A	01-Nov-26	09-Dec-25	28-Dec-25	140,091
Main Line Pipes		273	02-May-26 A	01-Nov-26	09-Dec-25	28-Dec-25	140,091
CO-R09.S01-IR-1	Installation Works for Main Line Valves of Irrigation Network-[Road 09] -[SW-1]	7	02-May-26 A	20-Oct-26	09-Dec-25	16-Dec-25	118,784
CO-R09.S01-IR-1	Trench Backfilling and Compaction Works for Main Lines of Irrigation Network-[Road	10	21-Oct-26	01-Nov-26	17-Dec-25	28-Dec-25	21,307
Street Lighting Network		10	02-Nov-26	12-Nov-26	29-Dec-25	08-Jan-26	4,664
Lighting Poles Works		10	02-Nov-26	12-Nov-26	29-Dec-25	08-Jan-26	4,664
CO-R09.S01-SL-	Foundation Excavation Works for Lighting Poles of Street Lighting Network-[Road 09	10	02-Nov-26	12-Nov-26	29-Dec-25	08-Jan-26	4,664
Medium Voltage Network		322	30-Sep-26 A	19-Dec-26	14-Feb-26	23-Feb-26	884,243
Cabling Works		322	30-Sep-26 A	19-Dec-26	14-Feb-26	23-Feb-26	884,243
CO-R09.S01-MV-	Trench Excavation and Bedding Works for Medium Voltage Network-[Road 09] -[SW	4	30-Sep-26 A	17-Dec-26	14-Feb-26	17-Feb-26	138,631
CO-R09.S01-MV-	Cable Laying Works for Medium Voltage Network-[Road 09] -[SW-1]	5	07-Oct-26 A	19-Dec-26	18-Feb-26	23-Feb-26	745,612
Road Works		82	10-Jun-26 A	11-Sep-27	21-Jun-26	24-Sep-26	738,543
Pre-Bituminous Construction		21	10-Jun-26 A	09-Feb-27	21-Jun-26	14-Jul-26	524,764
CO-R09.S01-RD-	Capping and Subgrade Layer for Road Works-[Road 09] -[SW-1]	21	10-Jun-26 A	09-Feb-27	21-Jun-26	14-Jul-26	524,764
Pavement Works		12	25-Aug-26 A	11-Sep-27	09-Sep-26	24-Sep-26	213,780
CO-R09.S01-RD-	Fixing of Interlock Tiles for Sidewalks Pavement-[Road 09] -[SW-1]	12	25-Aug-26 A	11-Sep-27	09-Sep-26	24-Sep-26	213,780
SW_2		394	10-Nov-25 A	11-Sep-27	21-Jul-25	01-Oct-26	1,200,937
Sewage Network		377	10-Nov-25 A	26-Oct-26	21-Jul-25	31-Aug-25	289,559
Main Line Sections		36	10-Nov-25 A	26-Oct-26	21-Jul-25	31-Aug-25	284,502
CO-R09.S02-SW-	Trench Excavation and Bedding Works for Main Lines of Sewage Network-[Road 09]	12	10-Nov-25 A	26-Oct-26	21-Jul-25	03-Aug-25	63,215
CO-R09.S02-SW-	Pipes Laying Works for Main Lines of Sewage Network-[Road 09]-[SW-2]	12	15-Feb-26 A	26-Oct-26	04-Aug-25	17-Aug-25	189,644
CO-R09.S02-SW-	Trench Backfilling and Compaction Works for Main Lines of Sewage Network-[Road (	12	02-May-26 A	26-Oct-26	18-Aug-25	31-Aug-25	31,643
Manholes		1	13-Oct-26	13-Oct-26	25-Aug-25	25-Aug-25	5,057
CO-R09.S02-SW-	Testing Works for Main Line Manholes of Sewage Network-[Road 09]-[SW-2]	1	13-Oct-26	13-Oct-26	25-Aug-25	25-Aug-25	5,057
Storm Drainage Network		298	24-Jun-26 A	25-Oct-26	23-Oct-25	20-Dec-25	287,863
Manholes		2	13-Oct-26	14-Oct-26	23-Oct-25	25-Oct-25	38,389
CO-R09.S02-SD-	Testing Works for Manholes of Storm Drainage Network-[Road 09]-[SW-2]	2	13-Oct-26	14-Oct-26	23-Oct-25	25-Oct-25	38,389
Catch Basin Sections		298	24-Jun-26 A	25-Oct-26	03-Nov-25	20-Dec-25	249,475
CO-R09.S02-SD-	Trench Excavation and Bedding Works for Catch Basins of Storm Drainage Network-	6	24-Jun-26 A	19-Oct-26	03-Nov-25	09-Nov-25	41,579
CO-R09.S02-SD-	Installation and Pipes Laying Connection Works for Catch Basins of Storm Drainage	7	25-Jun-26 A	20-Oct-26	30-Nov-25	07-Dec-25	124,737
CO-R09.S02-SD-	Trench Backfilling and Compaction Works for Catch Basins of Storm Drainage Netwc	7	28-Jun-26 A	25-Oct-26	13-Dec-25	20-Dec-25	55,439
CO-R09.S02-SD-	Testing Works for Catch Basins of Storm Drainage Network-[Road 09]-[SW-2]	4	21-Oct-26	25-Oct-26	08-Dec-25	11-Dec-25	27,719
Potable Water Network		305	27-Jun-26 A	21-Mar-27	03-Nov-25	29-Dec-25	409,735
Main Line Sections		49	27-Jun-26 A	21-Mar-27	03-Nov-25	29-Dec-25	254,908
CO-R09.S02-PW-	Trench Excavation and Bedding Works for Main Lines of Potable Water Network-[Ro	7	27-Jun-26 A	20-Oct-26	03-Nov-25	10-Nov-25	78,464
CO-R09.S02-PW-	Pipes Laying and accessories for Main Lines of Potable Water Network-[Road 09]-[	8	30-Jun-26 A	21-Mar-27	10-Dec-25	18-Dec-25	96,161
CO-R09.S02-PW-	Trench Backfilling and Compaction Works for Main Lines of Potable Water Network-[I	8	01-Jul-26 A	21-Mar-27	21-Dec-25	29-Dec-25	80,283
Valve Chamber		6	21-Oct-26	27-Oct-26	11-Nov-25	17-Nov-25	63,935
CO-R09.S02-PW-	Installation Works for Main Line Valves and Valve Chambers of Potable Water Netw	6	21-Oct-26	27-Oct-26	11-Nov-25	17-Nov-25	63,935
Fire Hydrant		11	21-Oct-26	02-Nov-26	11-Nov-25	23-Dec-25	90,892
CO-R09.S02-PW-	Excavation Works for Fire Hydrants of Potable Water Network-[Road 09]-[SW-2]	5	21-Oct-26	26-Oct-26	11-Nov-25	16-Nov-25	17,042
CO-R09.S02-PW-	Installation Works for Fire Hydrant of Potable Water Network-[Road 09]-[SW-2]	6	27-Oct-26	02-Nov-26	17-Dec-25	23-Dec-25	73,850
Road Works		18	25-Aug-26 A	11-Sep-27	09-Sep-26	01-Oct-26	213,780
Pavement Works		18	25-Aug-26 A	11-Sep-27	09-Sep-26	01-Oct-26	213,780
CO-R09.S02-RD-	Fixing of Interlock Tiles for Sidewalks Pavement-[Road 09]-[SW-2]	18	25-Aug-26 A	11-Sep-27	09-Sep-26	01-Oct-26	213,780
Road 10 Local 2 (2352 LM)		273	17-Jun-26 A	11-Jul-27	23-Jul-25	01-Oct-26	2,008,715
SW-3		54	25-Aug-26 A	11-Jul-27	15-Oct-25	29-Sep-26	614,524
SW_3-East		54	25-Aug-26 A	11-Jul-27	15-Oct-25	29-Sep-26	305,666
Potable Water Network		16	13-Oct-26	31-Oct-26	15-Oct-25	04-Nov-25	138,829
Valve Chamber		16	13-Oct-26	31-Oct-26	15-Oct-25	02-Nov-25	82,021
CO-R10.S03-ES	Excavation Works for Main Line Valves and Valve Chambers of Potable Water Netwc	1	13-Oct-26	13-Oct-26	15-Oct-25	15-Oct-25	1,161
CO-R10.S03-ES	RC Footing Works for Main Line Valves and Valve Chambers of Potable Water Netv	3	14-Oct-26	17-Oct-26	16-Oct-25	19-Oct-25	6,529
CO-R10.S03-ES	RC Wall Works for Main Line Valves and Valve Chambers of Potable Water Network	6	18-Oct-26	24-Oct-26	20-Oct-25	26-Oct-25	15,234

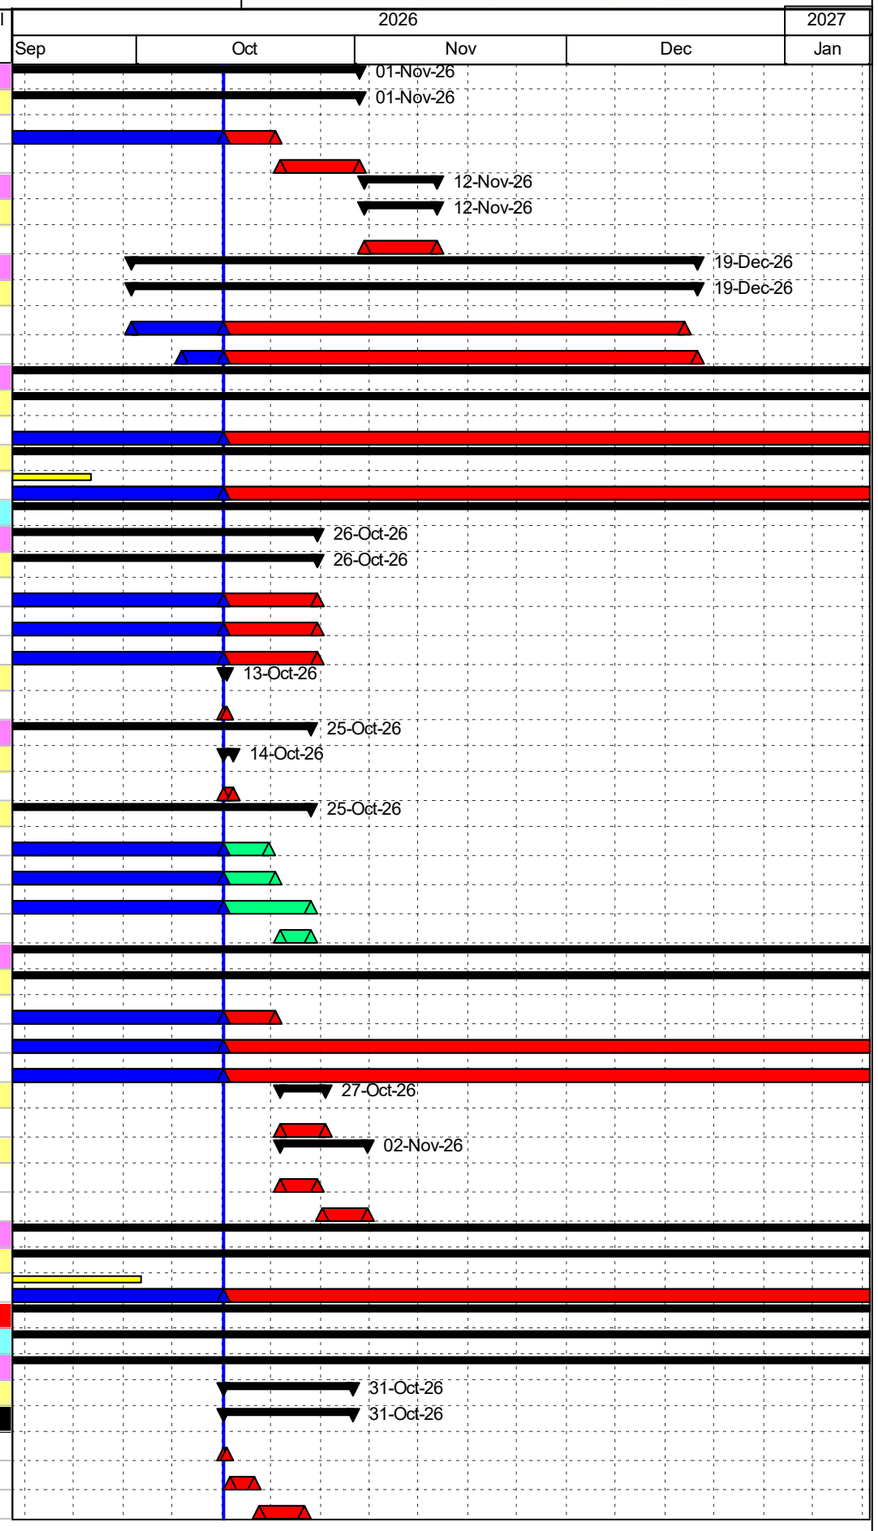


Primary Baseline
Actual Work
Summary
Remaining Work
Baseline Milestone
Critical Remaining Work
Milestone

Date	Revision	Checked	Approved
13-Oct-26	Third Industrial City		

Infrastructure Works of Area J -3rd Industrial City-
Dammam-Phase 2 - Update 13-10-2026
3Week Lookahead Schedule

Activity ID	Activity Name	Original Duration	Start	Finish	BL Project Start	BL Project Finish	Budgeted Total Cost
CO-R10.S03-ES	RC Slab Works for Main Line Valves and Valve Chambers of Potable Water Networl	2	25-Oct-26	26-Oct-26	27-Oct-25	28-Oct-25	8,705
CO-R10.S03-ES	Insulation Works for Main Line Valves and Valve Chambers of Potable Water Netwo	1	27-Oct-26	27-Oct-26	29-Oct-25	29-Oct-25	41,688
CO-R10.S03-ES	Backfilling Works for Main Line Valves and Valve Chambers of Potable Water Netwo	3	28-Oct-26	31-Oct-26	30-Oct-25	02-Nov-25	8,705
Fire Hydrant		15	13-Oct-26	29-Oct-26	19-Oct-25	04-Nov-25	56,808
CO-R10.S03-ES	Excavation Works for Fire Hydrants of Potable Water Network-[Road 10]-[SW-3]	6	13-Oct-26	19-Oct-26	19-Oct-25	25-Oct-25	8,521
CO-R10.S03-ES	Installation Works for Fire Hydrant of Potable Water Network-[Road 10]-[SW-3]	6	20-Oct-26	26-Oct-26	26-Oct-25	01-Nov-25	36,925
CO-R10.S03-ES	Trench Backfilling and Compaction Works for Fire Hydrants of Potable Water Networl	6	24-Oct-26	29-Oct-26	29-Oct-25	04-Nov-25	11,362
Street Lighting Network		33	13-Oct-26	19-Nov-26	02-Dec-25	16-Feb-26	59,654
Lighting Poles Works		33	13-Oct-26	19-Nov-26	02-Dec-25	16-Feb-26	59,654
CO-R10.S03-ES	Foundation Excavation Works for Lighting Poles of Street Lighting Network-[Road 1C	12	13-Oct-26	26-Oct-26	02-Dec-25	15-Dec-25	2,284
CO-R10.S03-ES	Installation Works for Lighting Poles Foundation of Street Lighting Network-[Road 10	12	19-Oct-26	01-Nov-26	08-Dec-25	21-Dec-25	8,731
CO-R10.S03-ES	Installation Works for Lighting Poles of Street Lighting Network-[Road 10]-[SW-3]	18	25-Oct-26	14-Nov-26	14-Dec-25	03-Jan-26	25,126
CO-R10.S03-ES	Installation Works for Lighting Fixtures With Drop Wire of Street Lighting Network-[Rc	18	31-Oct-26	19-Nov-26	26-Jan-26	16-Feb-26	14,376
CO-R10.S03-ES	Backfilling Works for Lighting Poles of Street Lighting Network-[Road 10]-[SW-3]	12	01-Nov-26	14-Nov-26	27-Jan-26	10-Feb-26	9,137
Road Works		10	25-Aug-26 A	11-Jul-27	17-Sep-26	29-Sep-26	107,184
Pavement Works		10	25-Aug-26 A	11-Jul-27	17-Sep-26	29-Sep-26	107,184
CO-R10.S03-ES	Fixing of Interlock Tiles for Sidewalks Pavement-[Road 10]-[SW-3]	10	25-Aug-26 A	11-Jul-27	17-Sep-26	29-Sep-26	107,184
SW_3-West		54	25-Aug-26 A	11-Jul-27	05-Jan-26	29-Sep-26	308,858
Potable Water Network		16	13-Oct-26	31-Oct-26	05-Jan-26	25-Jan-26	142,020
Valve Chamber		16	13-Oct-26	31-Oct-26	05-Jan-26	22-Jan-26	85,213
CO-R10.S03-WE	Excavation Works for Main Line Valves and Valve Chambers of Potable Water Netwc	1	13-Oct-26	13-Oct-26	05-Jan-26	05-Jan-26	4,352
CO-R10.S03-WE	RC Footing Works for Main Line Valves and Valve Chambers of Potable Water Netv	3	14-Oct-26	17-Oct-26	06-Jan-26	08-Jan-26	6,529
CO-R10.S03-WE	RC Wall Works for Main Line Valves and Valve Chambers of Potable Water Network	6	18-Oct-26	24-Oct-26	10-Jan-26	15-Jan-26	15,234
CO-R10.S03-WE	RC Slab Works for Main Line Valves and Valve Chambers of Potable Water Networl	2	25-Oct-26	26-Oct-26	17-Jan-26	18-Jan-26	8,705
CO-R10.S03-WE	Insulation Works for Main Line Valves and Valve Chambers of Potable Water Netwo	1	27-Oct-26	27-Oct-26	19-Jan-26	19-Jan-26	41,688
CO-R10.S03-WE	Backfilling Works for Main Line Valves and Valve Chambers of Potable Water Netwo	3	28-Oct-26	31-Oct-26	20-Jan-26	22-Jan-26	8,705
Fire Hydrant		15	13-Oct-26	29-Oct-26	08-Jan-26	25-Jan-26	56,808
CO-R10.S03-WE	Excavation Works for Fire Hydrants of Potable Water Network-[Road 10]-[SW-3]	6	13-Oct-26	19-Oct-26	08-Jan-26	14-Jan-26	8,521
CO-R10.S03-WE	Installation Works for Fire Hydrant of Potable Water Network-[Road 10]-[SW-3]	6	20-Oct-26	26-Oct-26	15-Jan-26	21-Jan-26	36,925
CO-R10.S03-WE	Trench Backfilling and Compaction Works for Fire Hydrants of Potable Water Networl	6	24-Oct-26	29-Oct-26	19-Jan-26	25-Jan-26	11,362
Street Lighting Network		33	13-Oct-26	19-Nov-26	22-Feb-26	04-Apr-26	59,654
Lighting Poles Works		33	13-Oct-26	19-Nov-26	22-Feb-26	04-Apr-26	59,654
CO-R10.S03-WE	Foundation Excavation Works for Lighting Poles of Street Lighting Network-[Road 1C	12	13-Oct-26	26-Oct-26	22-Feb-26	07-Mar-26	2,284
CO-R10.S03-WE	Installation Works for Lighting Poles Foundation of Street Lighting Network-[Road 10	12	19-Oct-26	01-Nov-26	28-Feb-26	12-Mar-26	8,731
CO-R10.S03-WE	Installation Works for Lighting Poles of Street Lighting Network-[Road 10]-[SW-3]	18	25-Oct-26	14-Nov-26	05-Mar-26	29-Mar-26	25,126
CO-R10.S03-WE	Installation Works for Lighting Fixtures With Drop Wire of Street Lighting Network-[Rc	18	31-Oct-26	19-Nov-26	11-Mar-26	04-Apr-26	14,376
CO-R10.S03-WE	Backfilling Works for Lighting Poles of Street Lighting Network-[Road 10]-[SW-3]	12	01-Nov-26	14-Nov-26	12-Mar-26	29-Mar-26	9,137
Road Works		10	25-Aug-26 A	11-Jul-27	17-Sep-26	29-Sep-26	107,184
Pavement Works		10	25-Aug-26 A	11-Jul-27	17-Sep-26	29-Sep-26	107,184
CO-R10.S03-WE	Fixing of Interlock Tiles for Sidewalks Pavement-[Road 10]-[SW-3]	10	25-Aug-26 A	11-Jul-27	17-Sep-26	29-Sep-26	107,184
SW-4		264	17-Jun-26 A	11-Jul-27	23-Jul-25	01-Oct-26	1,394,191
SW_4-East		236	21-Jun-26 A	11-Jul-27	23-Jul-25	29-Sep-26	638,054
Sewage Network		1	13-Oct-26	13-Oct-26	23-Jul-25	23-Jul-25	8,813
Manholes		1	13-Oct-26	13-Oct-26	23-Jul-25	23-Jul-25	8,813
CO-R10.S04-ES	Testing Works for Main Line Manholes of Sewage Network-[Road 10]-[SW-4]	1	13-Oct-26	13-Oct-26	23-Jul-25	23-Jul-25	8,813
Storm Drainage Network		10	13-Oct-26	24-Oct-26	18-Dec-25	22-Jan-26	34,251
Manholes		1	13-Oct-26	13-Oct-26	18-Dec-25	18-Dec-25	20,352
CO-R10.S04-ES	Testing Works for Manholes of Storm Drainage Network-[Road 10]-[SW-4]	1	13-Oct-26	13-Oct-26	18-Dec-25	18-Dec-25	20,352
Catch Basin Sections		10	13-Oct-26	24-Oct-26	12-Jan-26	22-Jan-26	13,899
CO-R10.S04-ES	Testing Works for Catch Basins of Storm Drainage Network-[Road 10]-[SW-4]	10	13-Oct-26	24-Oct-26	12-Jan-26	22-Jan-26	13,899
Potable Water Network		234	21-Jun-26 A	07-Nov-26	15-Jan-26	11-Feb-26	451,664
Valve Chamber		227	21-Jun-26 A	29-Oct-26	15-Jan-26	02-Feb-26	451,664

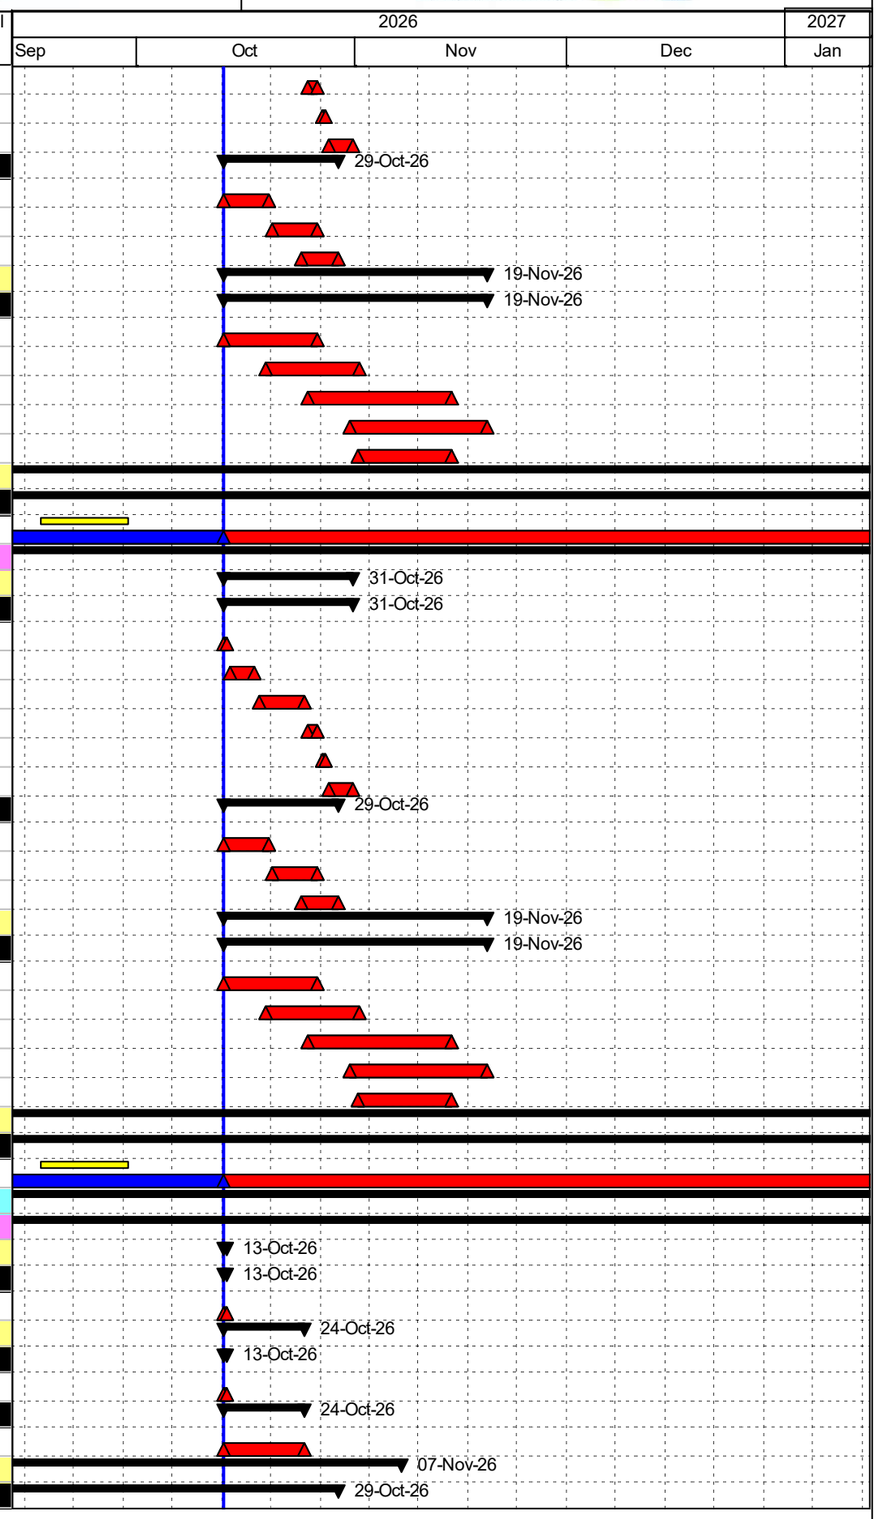


Primary Baseline | Actual Work | Summary
Remaining Work | Baseline Milestone
Critical Remaining Work | Milestone

Date	Revision	Checked	Approved
13-Oct-26	Third Industrial City		

Infrastructure Works of Area J -3rd Industrial City-
Dammam-Phase 2 - Update 13-10-2026
3Week Lookahead Schedule

Activity ID	Activity Name	Original Duration	Start	Finish	BL Project Start	BL Project Finish	Budgeted Total Cost
CO-R10.S04-ES	Insulation Works for Main Line Valves and Valve Chambers of Potable Water Netwo	1	21-Jun-26 A	26-Oct-26	29-Jan-26	29-Jan-26	319,299
CO-R10.S04-ES	Excavation Works for Main Line Valves and Valve Chambers of Potable Water Netw	1	13-Oct-26	13-Oct-26	15-Jan-26	15-Jan-26	16,109
CO-R10.S04-ES	RC Footing Works for Main Line Valves and Valve Chambers of Potable Water Netv	3	14-Oct-26	17-Oct-26	17-Jan-26	19-Jan-26	19,376
CO-R10.S04-ES	RC Wall Works for Main Line Valves and Valve Chambers of Potable Water Network	6	18-Oct-26	24-Oct-26	20-Jan-26	26-Jan-26	45,211
CO-R10.S04-ES	RC Slab Works for Main Line Valves and Valve Chambers of Potable Water Networl	2	25-Oct-26	26-Oct-26	27-Jan-26	28-Jan-26	25,835
CO-R10.S04-ES	Backfilling Works for Main Line Valves and Valve Chambers of Potable Water Netwo	3	27-Oct-26	29-Oct-26	31-Jan-26	02-Feb-26	25,835
Fire Hydrant		21	14-Oct-26	07-Nov-26	19-Jan-26	11-Feb-26	0
CO-R10.S04-ES	Excavation Works for Fire Hydrants of Potable Water Network-[Road 10]-[SW-4]	7	14-Oct-26	21-Oct-26	19-Jan-26	26-Jan-26	0
CO-R10.S04-ES	Installation Works for Fire Hydrant of Potable Water Network-[Road 10]-[SW-4]	7	22-Oct-26	29-Oct-26	27-Jan-26	03-Feb-26	0
CO-R10.S04-ES	Trench Backfilling and Compaction Works for Fire Hydrants of Potable Water Networl	7	31-Oct-26	07-Nov-26	04-Feb-26	11-Feb-26	0
Street Lighting Network		24	13-Oct-26	09-Nov-26	10-Mar-26	09-Apr-26	36,141
Lighting Poles Works		17	13-Oct-26	01-Nov-26	10-Mar-26	01-Apr-26	36,141
CO-R10.S04-ES	Foundation Excavation Works for Lighting Poles of Street Lighting Network-[Road 10	7	13-Oct-26	20-Oct-26	10-Mar-26	17-Mar-26	2,284
CO-R10.S04-ES	Installation Works for Lighting Poles Foundation of Street Lighting Network-[Road 10	7	19-Oct-26	26-Oct-26	16-Mar-26	26-Mar-26	8,731
CO-R10.S04-ES	Installation Works for Lighting Poles of Street Lighting Network-[Road 10]-[SW-4]	7	25-Oct-26	01-Nov-26	25-Mar-26	01-Apr-26	25,126
Cabling Works		7	02-Nov-26	09-Nov-26	02-Apr-26	09-Apr-26	0
CO-R10.S04-ES	Trench Excavation and Bedding Works for Street Lighting Network-[Road 10]-[SW-4]	7	02-Nov-26	09-Nov-26	02-Apr-26	09-Apr-26	0
Road Works		10	25-Aug-26 A	11-Jul-27	17-Sep-26	29-Sep-26	107,184
Pavement Works		10	25-Aug-26 A	11-Jul-27	17-Sep-26	29-Sep-26	107,184
CO-R10.S04-ES	Fixing of Interlock Tiles for Sidewalks Pavement-[Road 10]-[SW-4]	10	25-Aug-26 A	11-Jul-27	17-Sep-26	29-Sep-26	107,184
SW_4-West		262	17-Jun-26 A	11-Jul-27	11-Nov-25	01-Oct-26	756,137
Sewage Network		1	13-Oct-26	13-Oct-26	11-Nov-25	11-Nov-25	10,264
Manholes		1	13-Oct-26	13-Oct-26	11-Nov-25	11-Nov-25	10,264
CO-R10.S04-WE	Testing Works for Main Line Manholes of Sewage Network-[Road 10]-[SW-4]	1	13-Oct-26	13-Oct-26	11-Nov-25	11-Nov-25	10,264
Storm Drainage Network		247	17-Jun-26 A	20-Oct-26	18-Dec-25	26-Jan-26	147,127
Manholes		1	13-Oct-26	13-Oct-26	18-Dec-25	18-Dec-25	22,038
CO-R10.S04-WE	Testing Works for Manholes of Storm Drainage Network-[Road 10]-[SW-4]	1	13-Oct-26	13-Oct-26	18-Dec-25	18-Dec-25	22,038
Catch Basin Sections		247	17-Jun-26 A	20-Oct-26	28-Dec-25	26-Jan-26	125,090
CO-R10.S04-WE	Trench Excavation and Bedding Works for Catch Basins of Storm Drainage Network-	6	17-Jun-26 A	14-Oct-26	28-Dec-25	03-Jan-26	20,848
CO-R10.S04-WE	Installation and Pipes Laying Connection Works for Catch Basins of Storm Drainage	7	20-Jun-26 A	14-Oct-26	04-Jan-26	11-Jan-26	62,545
CO-R10.S04-WE	Testing Works for Catch Basins of Storm Drainage Network-[Road 10]-[SW-4]	10	23-Jun-26 A	15-Oct-26	12-Jan-26	22-Jan-26	13,899
CO-R10.S04-WE	Trench Backfilling and Compaction Works for Catch Basins of Storm Drainage Netwc	7	13-Oct-26	20-Oct-26	19-Jan-26	26-Jan-26	27,798
Potable Water Network		234	21-Jun-26 A	07-Nov-26	15-Jan-26	11-Feb-26	406,090
Valve Chamber		227	21-Jun-26 A	29-Oct-26	15-Jan-26	02-Feb-26	406,090
CO-R10.S04-WE	Insulation Works for Main Line Valves and Valve Chambers of Potable Water Netwo	1	21-Jun-26 A	26-Oct-26	29-Jan-26	29-Jan-26	319,299
CO-R10.S04-WE	Excavation Works for Main Line Valves and Valve Chambers of Potable Water Netw	1	13-Oct-26	13-Oct-26	15-Jan-26	15-Jan-26	8,679
CO-R10.S04-WE	RC Footing Works for Main Line Valves and Valve Chambers of Potable Water Netv	3	14-Oct-26	17-Oct-26	17-Jan-26	19-Jan-26	13,019
CO-R10.S04-WE	RC Wall Works for Main Line Valves and Valve Chambers of Potable Water Network	6	18-Oct-26	24-Oct-26	20-Jan-26	26-Jan-26	30,377
CO-R10.S04-WE	RC Slab Works for Main Line Valves and Valve Chambers of Potable Water Networl	2	25-Oct-26	26-Oct-26	27-Jan-26	28-Jan-26	17,358
CO-R10.S04-WE	Backfilling Works for Main Line Valves and Valve Chambers of Potable Water Netwo	3	27-Oct-26	29-Oct-26	31-Jan-26	02-Feb-26	17,358
Fire Hydrant		21	14-Oct-26	07-Nov-26	19-Jan-26	11-Feb-26	0
CO-R10.S04-WE	Excavation Works for Fire Hydrants of Potable Water Network-[Road 10]-[SW-4]	7	14-Oct-26	21-Oct-26	19-Jan-26	26-Jan-26	0
CO-R10.S04-WE	Installation Works for Fire Hydrant of Potable Water Network-[Road 10]-[SW-4]	7	22-Oct-26	29-Oct-26	27-Jan-26	03-Feb-26	0
CO-R10.S04-WE	Trench Backfilling and Compaction Works for Fire Hydrants of Potable Water Networl	7	31-Oct-26	07-Nov-26	04-Feb-26	11-Feb-26	0
Irrigation Network		13	21-Oct-26	04-Nov-26	12-Feb-26	26-Feb-26	85,471
Main Line Pipes		13	21-Oct-26	04-Nov-26	12-Feb-26	26-Feb-26	85,471
CO-R10.S04-WE	Trench Excavation and Bedding Works for Main Lines of Irrigation Network-[Road 10	6	21-Oct-26	27-Oct-26	12-Feb-26	18-Feb-26	21,368
CO-R10.S04-WE	Pipes Laying Works for Main Lines of Irrigation Network-[Road 10]-[SW-4]	7	28-Oct-26	04-Nov-26	19-Feb-26	26-Feb-26	64,103
Road Works		12	25-Aug-26 A	11-Jul-27	17-Sep-26	01-Oct-26	107,184
Pavement Works		12	25-Aug-26 A	11-Jul-27	17-Sep-26	01-Oct-26	107,184
CO-R10.S04-WE	Fixing of Interlock Tiles for Sidewalks Pavement-[Road 10]-[SW-4]	12	25-Aug-26 A	11-Jul-27	17-Sep-26	01-Oct-26	107,184
Road 11 Local 1 (670 LM)		335	02-Apr-26 A	02-Aug-27	04-Oct-25	13-Oct-26	333,551

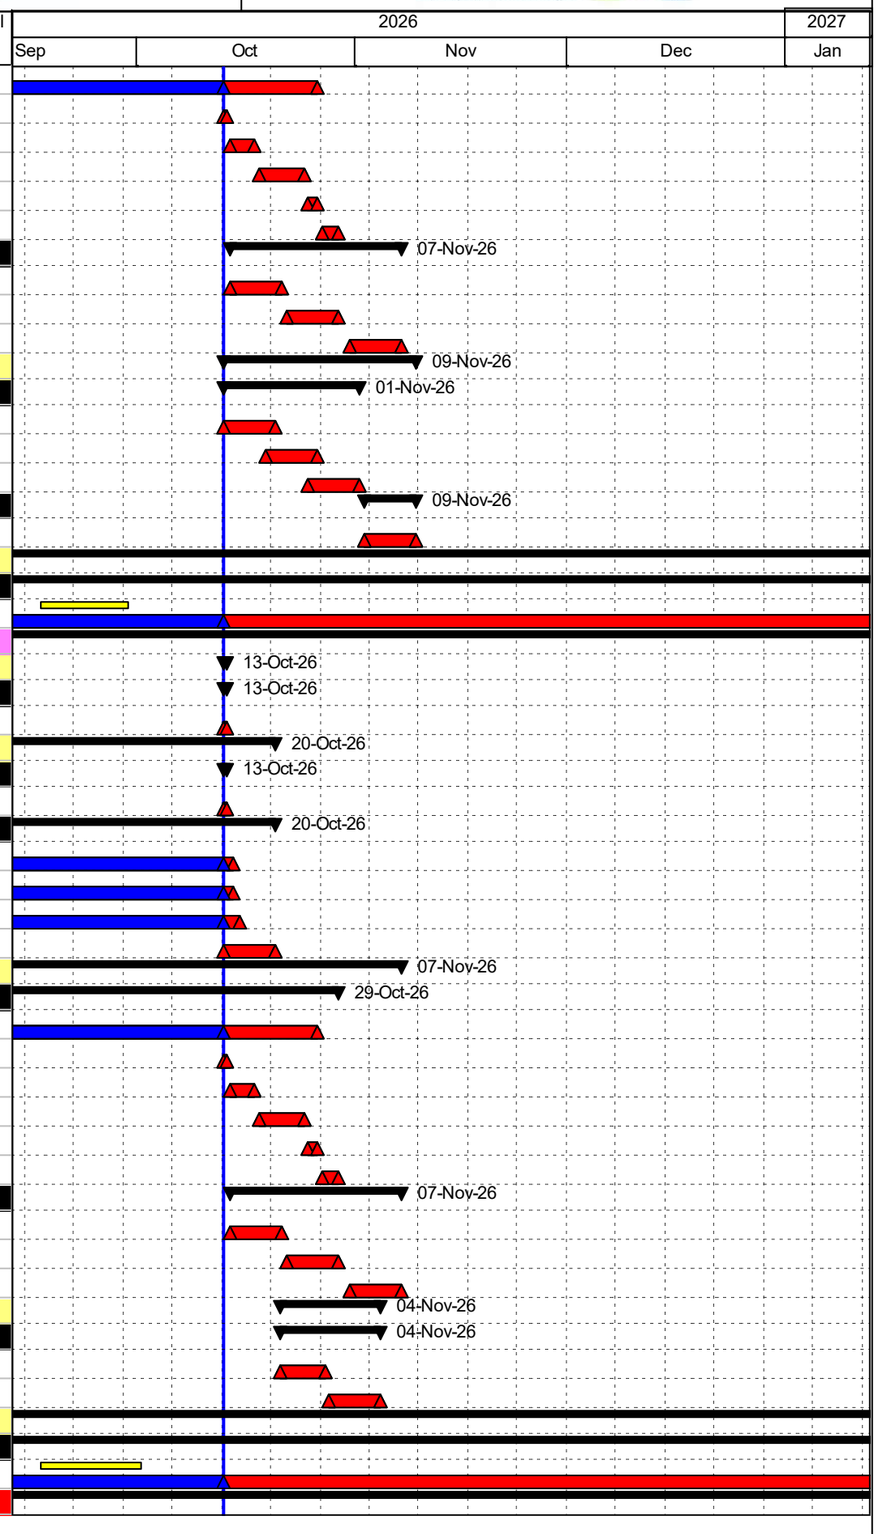


Primary Baseline
Remaining Work
Critical Remaining Work
Actual Work
Baseline Milestone
Milestone
Summary

Date	Revision	Checked	Approved
13-Oct-26	Third Industrial City		

Infrastructure Works of Area J -3rd Industrial City-
Dammam-Phase 2 - Update 13-10-2026
3Week Lookahead Schedule

Activity ID	Activity Name	Original Duration	Start	Finish	BL Project Start	BL Project Finish	Budgeted Total Cost
SW_5		245	25-Apr-26 A	02-Aug-27	03-Jan-26	11-Oct-26	148,458
Irrigation Network		245	25-Apr-26 A	24-Oct-26	03-Jan-26	21-Jan-26	85,996
Main Line Pipes		245	25-Apr-26 A	24-Oct-26	03-Jan-26	21-Jan-26	85,996
CO-R11.S05-IR-1	Pipes Laying Works for Main Lines of Irrigation Network-[Road 11]-[SW-5]	7	25-Apr-26 A	13-Oct-26	03-Jan-26	10-Jan-26	37,411
CO-R11.S05-IR-1	Installation Works for Main Line Valves of Irrigation Network-[Road 11]-[SW-5]	3	13-Oct-26	15-Oct-26	11-Jan-26	13-Jan-26	42,350
CO-R11.S05-IR-1	Trench Backfilling and Compaction Works for Main Lines of Irrigation Network-[Road	7	17-Oct-26	24-Oct-26	14-Jan-26	21-Jan-26	6,235
Road Works		10	25-Aug-26 A	02-Aug-27	30-Sep-26	11-Oct-26	62,462
Pavement Works		10	25-Aug-26 A	02-Aug-27	30-Sep-26	11-Oct-26	62,462
CO-R11.S05-RD-	Fixing of Interlock Tiles for Sidewalks Pavement-[Road 11]-[SW-5]	10	25-Aug-26 A	02-Aug-27	30-Sep-26	11-Oct-26	62,462
SW_6		335	02-Apr-26 A	02-Aug-27	04-Oct-25	13-Oct-26	185,092
Sewage Network		318	02-Apr-26 A	18-Oct-26	04-Oct-25	14-Oct-25	81,435
Manholes		318	02-Apr-26 A	18-Oct-26	04-Oct-25	14-Oct-25	81,435
CO-R11.S06-SW-	Install Grp Liner Wall Works for Main Line Manholes of Sewage Network-[Road 11]-[S	4	02-Apr-26 A	17-Oct-26	04-Oct-25	07-Oct-25	72,387
CO-R11.S06-SW-	Testing Works for Main Line Manholes of Sewage Network-[Road 11]-[SW-6]	1	18-Oct-26	18-Oct-26	14-Oct-25	14-Oct-25	9,048
Potable Water Network		6	13-Oct-26	19-Oct-26	28-Jan-26	03-Feb-26	15,887
Valve Chamber		6	13-Oct-26	19-Oct-26	28-Jan-26	03-Feb-26	15,887
CO-R11.S06-PW-	Installation Works for Main Line Valves and Valve Chambers of Potable Water Netw	6	13-Oct-26	19-Oct-26	28-Jan-26	03-Feb-26	15,887
Street Lighting Network		22	13-Oct-26	07-Nov-26	19-May-26	19-Jul-26	25,308
Lighting Poles Works		22	13-Oct-26	07-Nov-26	24-Jun-26	19-Jul-26	21,319
CO-R11.S06-SL-2	Backfilling Works for Lighting Poles of Street Lighting Network-[Road 11]-[SW-6]	15	13-Oct-26	29-Oct-26	24-Jun-26	11-Jul-26	10,659
CO-R11.S06-SL-2	Testing Works for Lighting Poles of Street Lighting Network-[Road 11]-[SW-6]	7	31-Oct-26	07-Nov-26	12-Jul-26	19-Jul-26	10,659
Cabling Works		10	13-Oct-26	24-Oct-26	19-May-26	03-Jun-26	3,989
CO-R11.S06-SL-1	Trench Backfilling and Compaction Works for Street Lighting Network-[Road 11]-[SW	10	13-Oct-26	24-Oct-26	19-May-26	03-Jun-26	3,989
Road Works		10	25-Aug-26 A	02-Aug-27	03-Oct-26	13-Oct-26	62,462
Pavement Works		10	25-Aug-26 A	02-Aug-27	03-Oct-26	13-Oct-26	62,462
CO-R11.S06-RD-	Fixing of Interlock Tiles for Sidewalks Pavement-[Road 11]-[SW-6]	10	25-Aug-26 A	02-Aug-27	03-Oct-26	13-Oct-26	62,462
Road 14 Local 1 (584 LM)		25	25-Aug-26 A	16-Aug-27	02-Aug-25	27-Oct-26	271,925
SW_7		25	25-Aug-26 A	16-Aug-27	02-Aug-25	25-Oct-26	108,146
Sewage Network		1	13-Oct-26	13-Oct-26	01-Sep-25	01-Sep-25	6,319
Manholes		1	13-Oct-26	13-Oct-26	01-Sep-25	01-Sep-25	6,319
CO-R14.S07-SW-	Testing Works for Main Line Manholes of Sewage Network-[Road 14]-[SW-7]	1	13-Oct-26	13-Oct-26	01-Sep-25	01-Sep-25	6,319
Street Lighting Network		24	13-Oct-26	09-Nov-26	02-Aug-25	11-Jun-26	9,399
Lighting Poles Works		18	13-Oct-26	02-Nov-26	18-May-26	11-Jun-26	9,399
CO-R14.S07-SL-	Installation Works for Lighting Fixtures With Drop Wire of Street Lighting Network-[Rc	18	13-Oct-26	02-Nov-26	18-May-26	11-Jun-26	7,713
CO-R14.S07-SL-2	Testing Works for Lighting Poles of Street Lighting Network-[Road 14]-[SW-7]	5	13-Oct-26	18-Oct-26	07-Jun-26	11-Jun-26	1,686
Distrubution Panel Boards		24	13-Oct-26	09-Nov-26	02-Aug-25	28-Aug-25	0
CO-R14.S07-SL-	Foundation Excavation Works For Panel Boards of Street Lighting Network-[Road 14	18	13-Oct-26	02-Nov-26	02-Aug-25	21-Aug-25	0
CO-R14.S07-SL-	Installation Works for Panel Board Concrete Foundations of Street Lighting Network-	18	17-Oct-26	05-Nov-26	05-Aug-25	25-Aug-25	0
CO-R14.S07-SL-2	A wall of concrete blocks to install the KWH meter of Street Lighting Network-[Road 1	18	17-Oct-26	05-Nov-26	05-Aug-25	25-Aug-25	0
CO-R14.S07-SL-	Installation Works for Lighting Panel Boards of Street Lighting Network-[Road 14]-[S\	18	20-Oct-26	09-Nov-26	09-Aug-25	28-Aug-25	0
Road Works		12	25-Aug-26 A	16-Aug-27	12-Oct-26	25-Oct-26	92,428
Pavement Works		12	25-Aug-26 A	16-Aug-27	12-Oct-26	25-Oct-26	92,428
CO-R14.S07-RD-	Fixing of Interlock Tiles for Sidewalks Pavement-[Road 14]-[SW-7]	12	25-Aug-26 A	16-Aug-27	12-Oct-26	25-Oct-26	92,428
SW_8		21	25-Aug-26 A	16-Aug-27	15-Sep-25	27-Oct-26	163,779
Sewage Network		1	13-Oct-26	13-Oct-26	15-Sep-25	15-Sep-25	2,342
Manholes		1	13-Oct-26	13-Oct-26	15-Sep-25	15-Sep-25	2,342
CO-R14.S08-SW-	Testing Works for Main Line Manholes of Sewage Network-[Road 14]-[SW-8]	1	13-Oct-26	13-Oct-26	15-Sep-25	15-Sep-25	2,342
Potable Water Network		21	13-Oct-26	05-Nov-26	26-Feb-26	25-Mar-26	53,020
Fire Hydrant		21	13-Oct-26	05-Nov-26	26-Feb-26	25-Mar-26	53,020
CO-R14.S08-PW-	Excavation Works for Fire Hydrants of Potable Water Network-[Road 14]-[SW-8]	7	13-Oct-26	20-Oct-26	26-Feb-26	05-Mar-26	7,953
CO-R14.S08-PW-	Installation Works for Fire Hydrant of Potable Water Network-[Road 14]-[SW-8]	7	21-Oct-26	28-Oct-26	07-Mar-26	14-Mar-26	34,463
CO-R14.S08-PW-	Trench Backfilling and Compaction Works for Fire Hydrants of Potable Water Networl	7	29-Oct-26	05-Nov-26	15-Mar-26	25-Mar-26	10,604
Street Lighting Network		7	13-Oct-26	20-Oct-26	24-Jun-26	01-Jul-26	15,989

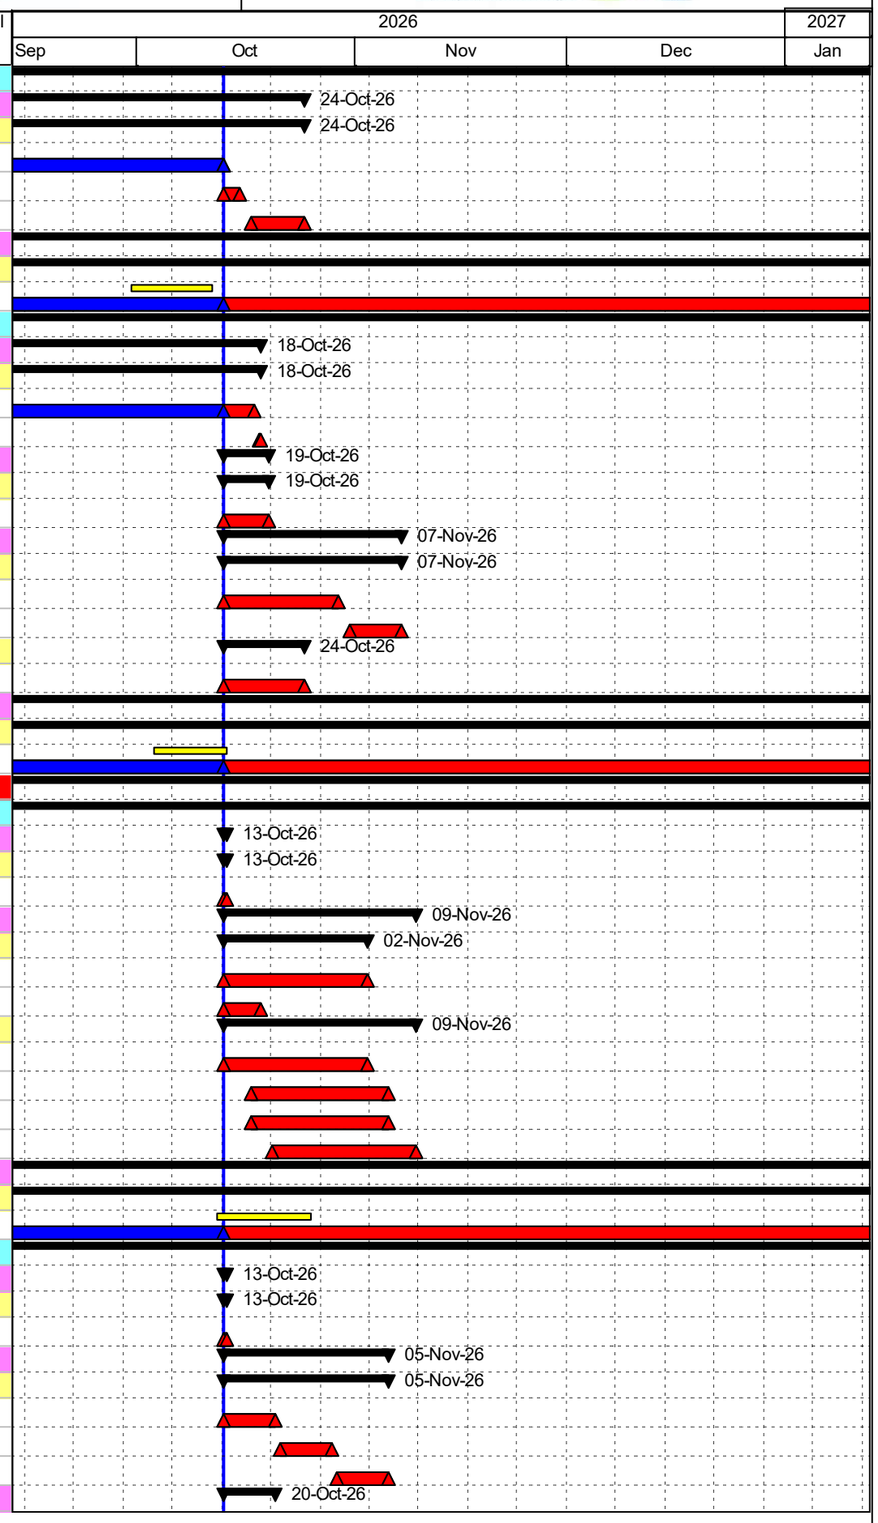


Primary Baseline | Actual Work | Summary
Remaining Work | Baseline Milestone
Critical Remaining Work | Milestone

Date	Revision	Checked	Approved
13-Oct-26	Third Industrial City		

Infrastructure Works of Area J -3rd Industrial City-
Dammam-Phase 2 - Update 13-10-2026
3Week Lookahead Schedule


Activity ID	Activity Name	Original Duration	Start	Finish	BL Project Start	BL Project Finish	Budgeted Total Cost
Lighting Poles Works		7	13-Oct-26	20-Oct-26	24-Jun-26	01-Jul-26	15,989
CO-R14.S08-SL-:	Testing Works for Lighting Poles of Street Lighting Network-[Road 14]-[SW-8]	7	13-Oct-26	20-Oct-26	24-Jun-26	01-Jul-26	15,989
Road Works		12	25-Aug-26 A	16-Aug-27	14-Oct-26	27-Oct-26	92,428
Pavement Works		12	25-Aug-26 A	16-Aug-27	14-Oct-26	27-Oct-26	92,428
CO-R14.S08-RD-	Fixing of Interlock Tiles for Sidewalks Pavement-[Road 14]-[SW-8]	12	25-Aug-26 A	16-Aug-27	14-Oct-26	27-Oct-26	92,428
Road 15 Local 1 (556 LM)		24	25-Aug-26 A	01-Sep-27	02-Jun-25	08-Nov-26	165,086
SW_9		12	25-Aug-26 A	01-Sep-27	26-Oct-26	08-Nov-26	52,781
Road Works		12	25-Aug-26 A	01-Sep-27	26-Oct-26	08-Nov-26	52,781
Pavement Works		12	25-Aug-26 A	01-Sep-27	26-Oct-26	08-Nov-26	52,781
CO-R15.S09-RD-	Fixing of Interlock Tiles for Sidewalks Pavement-[Road 15]-[SW-9]	12	25-Aug-26 A	01-Sep-27	26-Oct-26	08-Nov-26	52,781
SW_10		24	25-Aug-26 A	01-Sep-27	02-Jun-25	08-Nov-26	112,304
Sewage Network		1	13-Oct-26	13-Oct-26	05-Jul-25	06-Jul-25	2,883
Manholes		1	13-Oct-26	13-Oct-26	05-Jul-25	06-Jul-25	2,883
CO-R15.S10-SW-	Testing Works for Main Line Manholes of Sewage Network-[Road 15]-[SW-10]	1	13-Oct-26	13-Oct-26	05-Jul-25	06-Jul-25	2,883
Street Lighting Network		24	13-Oct-26	09-Nov-26	02-Jun-25	02-Feb-26	26,343
Lighting Poles Works		5	13-Oct-26	18-Oct-26	27-Jan-26	02-Feb-26	9,517
CO-R15.S10-SL-:	Testing Works for Lighting Poles of Street Lighting Network-[Road 15]-[SW-10]	5	13-Oct-26	18-Oct-26	27-Jan-26	02-Feb-26	9,517
Distrubution Panel Boards		24	13-Oct-26	09-Nov-26	02-Jun-25	03-Jul-25	16,825
CO-R15.S10-SL-:	Foundation Excavation Works For Panel Boards of Street Lighting Network-[Road 15	18	13-Oct-26	02-Nov-26	02-Jun-25	26-Jun-25	0
CO-R15.S10-SL-:	Installation Works for Panel Board Concrete Foundations of Street Lighting Network-	18	17-Oct-26	05-Nov-26	10-Jun-25	30-Jun-25	0
CO-R15.S10-SL-:	A wall of concrete blocks to install the KWH meter of Street Lighting Network-[Road 1	18	17-Oct-26	05-Nov-26	10-Jun-25	30-Jun-25	16,825
CO-R15.S10-SL-:	Installation Works for Lighting Panel Boards of Street Lighting Network-[Road 15]-[S\	18	20-Oct-26	09-Nov-26	14-Jun-25	03-Jul-25	0
Potable Water Network		18	14-Oct-26	03-Nov-26	08-Mar-26	31-Mar-26	30,297
Fire Hydrant		18	14-Oct-26	03-Nov-26	08-Mar-26	31-Mar-26	30,297
CO-R15.S10-PW-	Excavation Works for Fire Hydrants of Potable Water Network-[Road 15]-[SW-10]	6	14-Oct-26	20-Oct-26	08-Mar-26	14-Mar-26	4,545
CO-R15.S10-PW-	Installation Works for Fire Hydrant of Potable Water Network-[Road 15]-[SW-10]	6	21-Oct-26	27-Oct-26	15-Mar-26	24-Mar-26	19,693
CO-R15.S10-PW-	Trench Backfilling and Compaction Works for Fire Hydrants of Potable Water Networl	6	28-Oct-26	03-Nov-26	25-Mar-26	31-Mar-26	6,059
Road Works		10	25-Aug-26 A	01-Sep-27	28-Oct-26	08-Nov-26	52,781
Pavement Works		10	25-Aug-26 A	01-Sep-27	28-Oct-26	08-Nov-26	52,781
CO-R15.S10-RD-	Fixing of Interlock Tiles for Sidewalks Pavement-[Road 15]-[SW-10]	10	25-Aug-26 A	01-Sep-27	28-Oct-26	08-Nov-26	52,781
Road 16 Local 1 (527 LM)		33	25-Aug-26 A	15-Sep-27	29-Mar-26	19-Nov-26	124,974
SW_11		10	25-Aug-26 A	15-Sep-27	05-Nov-26	16-Nov-26	50,368
Road Works		10	25-Aug-26 A	15-Sep-27	05-Nov-26	16-Nov-26	50,368
Pavement Works		10	25-Aug-26 A	15-Sep-27	05-Nov-26	16-Nov-26	50,368
CO-R16.S11-RD-	Fixing of Interlock Tiles for Sidewalks Pavement-[Road 16]-[SW-11]	10	25-Aug-26 A	15-Sep-27	05-Nov-26	16-Nov-26	50,368
SW_12		33	25-Aug-26 A	15-Sep-27	29-Mar-26	19-Nov-26	74,606
Potable Water Network		19	13-Oct-26	03-Nov-26	29-Mar-26	11-Apr-26	24,238
Fire Hydrant		19	13-Oct-26	03-Nov-26	29-Mar-26	11-Apr-26	24,238
CO-R16.S12-PW-	Excavation Works for Fire Hydrants of Potable Water Network-[Road 16]-[SW-12]	6	13-Oct-26	19-Oct-26	29-Mar-26	04-Apr-26	4,545
CO-R16.S12-PW-	Installation Works for Fire Hydrant of Potable Water Network-[Road 16]-[SW-12]	6	28-Oct-26	03-Nov-26	05-Apr-26	11-Apr-26	19,693
Road Works		10	25-Aug-26 A	15-Sep-27	09-Nov-26	19-Nov-26	50,368
Pavement Works		10	25-Aug-26 A	15-Sep-27	09-Nov-26	19-Nov-26	50,368
CO-R16.S12-RD-	Fixing of Interlock Tiles for Sidewalks Pavement-[Road 16]-[SW-12]	10	25-Aug-26 A	15-Sep-27	09-Nov-26	19-Nov-26	50,368
Road 17 Local 1 (500 LM)		24	13-Oct-26	09-Nov-26	16-Apr-25	01-Sep-26	55,889
SW_14		24	13-Oct-26	09-Nov-26	16-Apr-25	01-Sep-26	55,889
Sewage Network		1	13-Oct-26	13-Oct-26	21-May-25	21-May-25	1,518
Manholes		1	13-Oct-26	13-Oct-26	21-May-25	21-May-25	1,518
CO-R17.S14-SW-	Testing Works for Main Line Manholes of Sewage Network-[Road 17]-[SW-14]	1	13-Oct-26	13-Oct-26	21-May-25	21-May-25	1,518
Street Lighting Network		24	13-Oct-26	09-Nov-26	16-Apr-25	14-Dec-25	44,704
Lighting Poles Works		5	13-Oct-26	18-Oct-26	08-Dec-25	14-Dec-25	17,131
CO-R17.S14-SL-:	Testing Works for Lighting Poles of Street Lighting Network-[Road 17]-[SW-14]	5	13-Oct-26	18-Oct-26	08-Dec-25	14-Dec-25	17,131
Distrubution Panel Boards		24	13-Oct-26	09-Nov-26	16-Apr-25	13-May-25	27,573
CO-R17.S14-SL-:	Foundation Excavation Works For Panel Boards of Street Lighting Network-[Road 17	18	13-Oct-26	02-Nov-26	16-Apr-25	06-May-25	0
CO-R17.S14-SL-:	Installation Works for Panel Board Concrete Foundations of Street Lighting Network-	18	17-Oct-26	05-Nov-26	20-Apr-25	10-May-25	0

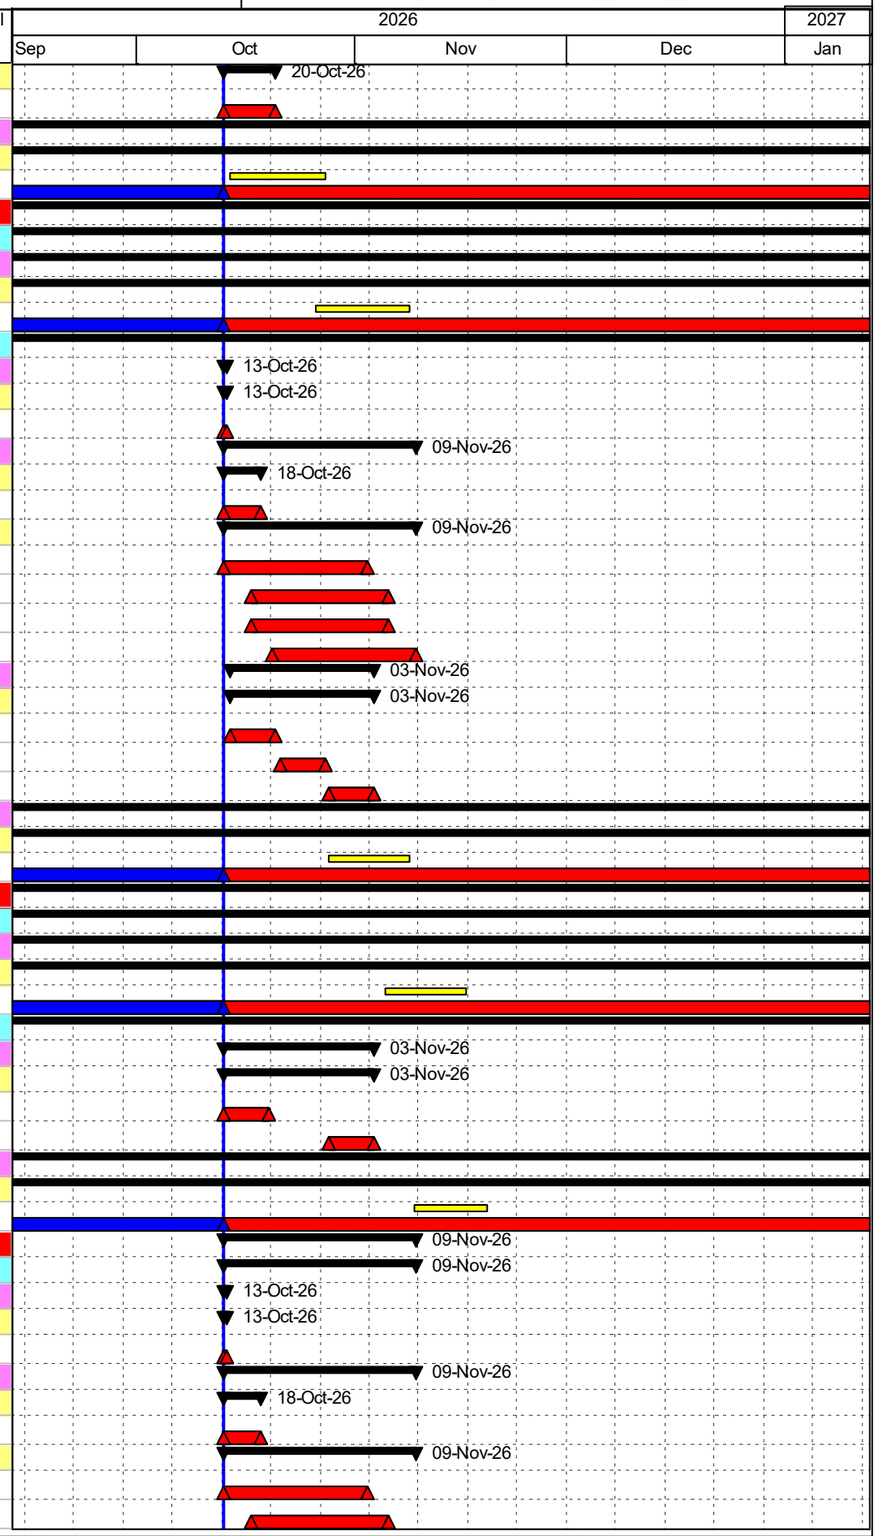

Primary Baseline
Remaining Work
Critical Remaining Work
Actual Work
Baseline Milestone
Milestone
Summary

Date	Revision	Checked	Approved
13-Oct-26	Third Industrial City		

Activity ID	Activity Name	Original Duration	Start	Finish	BL Project Start	BL Project Finish	Budgeted Total Cost
CO-R17.S14-SL-;	A wall of concrete blocks to install the KWH meter of Street Lighting Network-[Road 1	18	17-Oct-26	05-Nov-26	20-Apr-25	10-May-25	27,573
CO-R17.S14-SL-	Installation Works for Lighting Panel Boards of Street Lighting Network-[Road 17]-[S\	18	20-Oct-26	09-Nov-26	23-Apr-25	13-May-25	0
Potable Water Network		6	14-Oct-26	20-Oct-26	21-Apr-26	27-Apr-26	3,408
Fire Hydrant		6	14-Oct-26	20-Oct-26	21-Apr-26	27-Apr-26	3,408
CO-R17.S14-PW-	Excavation Works for Fire Hydrants of Potable Water Network-[Road 17]-[SW-14]	6	14-Oct-26	20-Oct-26	21-Apr-26	27-Apr-26	3,408
Telecom Network		21	13-Oct-26	05-Nov-26	09-Aug-26	01-Sep-26	6,258
Manholes Works		21	13-Oct-26	05-Nov-26	09-Aug-26	01-Sep-26	6,258
CO-R17.S14-TE-	Excavation Works for Manholes of Telecom Network-[Road 17]-[SW-14]	7	13-Oct-26	20-Oct-26	09-Aug-26	16-Aug-26	628
CO-R17.S14-TE-	Installation Works for Manholes of Telecom Network-[Road 17]-[SW-14]	7	21-Oct-26	28-Oct-26	17-Aug-26	24-Aug-26	5,002
CO-R17.S14-TE-	Backfilling Works for Manholes of Telecom Network-[Road 17]-[SW-14]	7	29-Oct-26	05-Nov-26	25-Aug-26	01-Sep-26	628
Road 18 Local 1 (479 LM)		35	13-Oct-26	22-Nov-26	19-Mar-25	27-Nov-25	51,658
SW_16		35	13-Oct-26	22-Nov-26	19-Mar-25	27-Nov-25	51,658
Street Lighting Network		35	13-Oct-26	22-Nov-26	19-Mar-25	27-Nov-25	36,510
Lighting Poles Works		35	13-Oct-26	22-Nov-26	08-Nov-25	27-Nov-25	20,573
CO-R18.S16-SL-;	Testing Works for Lighting Poles of Street Lighting Network-[Road 18]-[SW-16]	5	13-Oct-26	18-Oct-26	22-Nov-25	27-Nov-25	7,995
CO-R18.S16-SL-	Installation Works for Lighting Fixtures With Drop Wire of Street Lighting Network-[Rc	18	02-Nov-26	22-Nov-26	08-Nov-25	27-Nov-25	12,579
Distrubution Panel Boards		24	13-Oct-26	09-Nov-26	19-Mar-25	20-Apr-25	15,936
CO-R18.S16-SL-	Foundation Excavation Works For Panel Boards of Street Lighting Network-[Road 18	18	13-Oct-26	02-Nov-26	19-Mar-25	13-Apr-25	0
CO-R18.S16-SL-	Installation Works for Panel Board Concrete Foundations of Street Lighting Network-	18	17-Oct-26	05-Nov-26	23-Mar-25	16-Apr-25	0
CO-R18.S16-SL-;	A wall of concrete blocks to install the KWH meter of Street Lighting Network-[Road 1	18	17-Oct-26	05-Nov-26	23-Mar-25	16-Apr-25	15,936
CO-R18.S16-SL-	Installation Works for Lighting Panel Boards of Street Lighting Network-[Road 18]-[S\	18	20-Oct-26	09-Nov-26	26-Mar-25	20-Apr-25	0
Potable Water Network		18	13-Oct-26	02-Nov-26	23-Aug-25	11-Sep-25	15,149
Fire Hydrant		18	13-Oct-26	02-Nov-26	23-Aug-25	11-Sep-25	15,149
CO-R18.S16-PW-	Excavation Works for Fire Hydrants of Potable Water Network-[Road 18]-[SW-16]	6	13-Oct-26	19-Oct-26	23-Aug-25	28-Aug-25	2,272
CO-R18.S16-PW-	Installation Works for Fire Hydrant of Potable Water Network-[Road 18]-[SW-16]	6	20-Oct-26	26-Oct-26	30-Aug-25	04-Sep-25	9,847
CO-R18.S16-PW-	Trench Backfilling and Compaction Works for Fire Hydrants of Potable Water Networl	6	27-Oct-26	02-Nov-26	06-Sep-25	11-Sep-25	3,030
Finishes for Infrastructure Networks		83	01-Jun-26 A	29-Jun-27	15-Jul-26	03-Oct-26	1,796,956
Phase 2 Block "J"		83	01-Jun-26 A	29-Jun-27	15-Jul-26	03-Oct-26	1,796,956
Road 09 Local 2 (2278 LM)		43	01-Jun-26 A	29-Jun-27	15-Jul-26	02-Sep-26	967,473
Sewage Network		12	01-Jun-26 A	10-Jun-27	19-Jul-26	01-Aug-26	208,794
Testing and Finishes		12	01-Jun-26 A	10-Jun-27	19-Jul-26	01-Aug-26	208,794
CO-R09-SW-TF-1	Final Testing For Main Line of Sewage Network-[Road 09]	12	01-Jun-26 A	10-Jun-27	19-Jul-26	01-Aug-26	208,794
Storm Drainage Network		43	17-Jun-26 A	29-Jun-27	15-Jul-26	02-Sep-26	758,679
Testing and Finishes		43	17-Jun-26 A	29-Jun-27	15-Jul-26	02-Sep-26	758,679
CO-R09-SD-TF-1	Testing Work for Pipes of Storm Drainage Network-[Road 09]	12	17-Jun-26 A	12-Jun-27	19-Jul-26	01-Aug-26	101,957
CO-R09-SD-TF-1	Install Catch Basin Cover Works for External Finishes of Storm Drainage Network-[R	16	20-Jun-26 A	01-Apr-27	15-Jul-26	02-Aug-26	27,719
CO-R09-SD-TF-1	Main Manhole Internal Finishes (Benching + Insulation) for Storm Drainage Network	16	21-Jun-26 A	29-Jun-27	16-Aug-26	02-Sep-26	601,283
CO-R09-SD-TF-1	Catch Basin Internal Finishes (Benching + Insulation) for Storm Drainage Network-[F	16	22-Jun-26 A	29-Jun-27	16-Aug-26	02-Sep-26	27,719
Road 10 Local 2 (2352 LM)		66	17-Jun-26 A	31-May-27	04-Aug-26	16-Sep-26	558,233
Storm Drainage Network		35	17-Jun-26 A	31-May-27	04-Aug-26	13-Sep-26	558,233
Testing and Finishes		35	17-Jun-26 A	31-May-27	04-Aug-26	13-Sep-26	558,233
CO-R10-SD-TF-1	Install Catch Basin Cover Works for External Finishes of Storm Drainage Network-[R	16	17-Jun-26 A	11-May-27	04-Aug-26	22-Aug-26	27,796
CO-R10-SD-TF-1	Main Manhole Internal Finishes (Benching + Insulation) for Storm Drainage Network	12	18-Jun-26 A	31-May-27	26-Aug-26	08-Sep-26	502,642
CO-R10-SD-TF-1	Catch Basin Internal Finishes (Benching + Insulation) for Storm Drainage Network-[F	16	22-Jun-26 A	31-May-27	26-Aug-26	13-Sep-26	27,795
Medium Voltage Network		7	13-Oct-26	20-Oct-26	09-Sep-26	16-Sep-26	0
Termination and Testing Works		7	13-Oct-26	20-Oct-26	09-Sep-26	16-Sep-26	0
CO-R10-MV-TF-1	Termination Works of Medium Voltage Network-[Road 10]	7	13-Oct-26	20-Oct-26	09-Sep-26	16-Sep-26	0
Road 11 Local 1 (670 LM)		35	22-Jun-26 A	14-Jun-27	23-Aug-26	03-Oct-26	271,250
Storm Drainage Network		35	22-Jun-26 A	14-Jun-27	23-Aug-26	03-Oct-26	271,250
Testing and Finishes		35	22-Jun-26 A	14-Jun-27	23-Aug-26	03-Oct-26	271,250
CO-R11-SD-TF-1	Catch Basin Internal Finishes (Benching + Insulation) for Storm Drainage Network-[F	16	22-Jun-26 A	14-Jun-27	14-Sep-26	03-Oct-26	8,112
CO-R11-SD-TF-1	Main Manhole Internal Finishes (Benching + Insulation) for Storm Drainage Network	12	23-Jun-26 A	14-Jun-27	09-Sep-26	22-Sep-26	255,027
CO-R11-SD-TF-1	Install Catch Basin Cover Works for External Finishes of Storm Drainage Network-[R	12	27-Jun-26 A	06-May-27	23-Aug-26	05-Sep-26	8,112

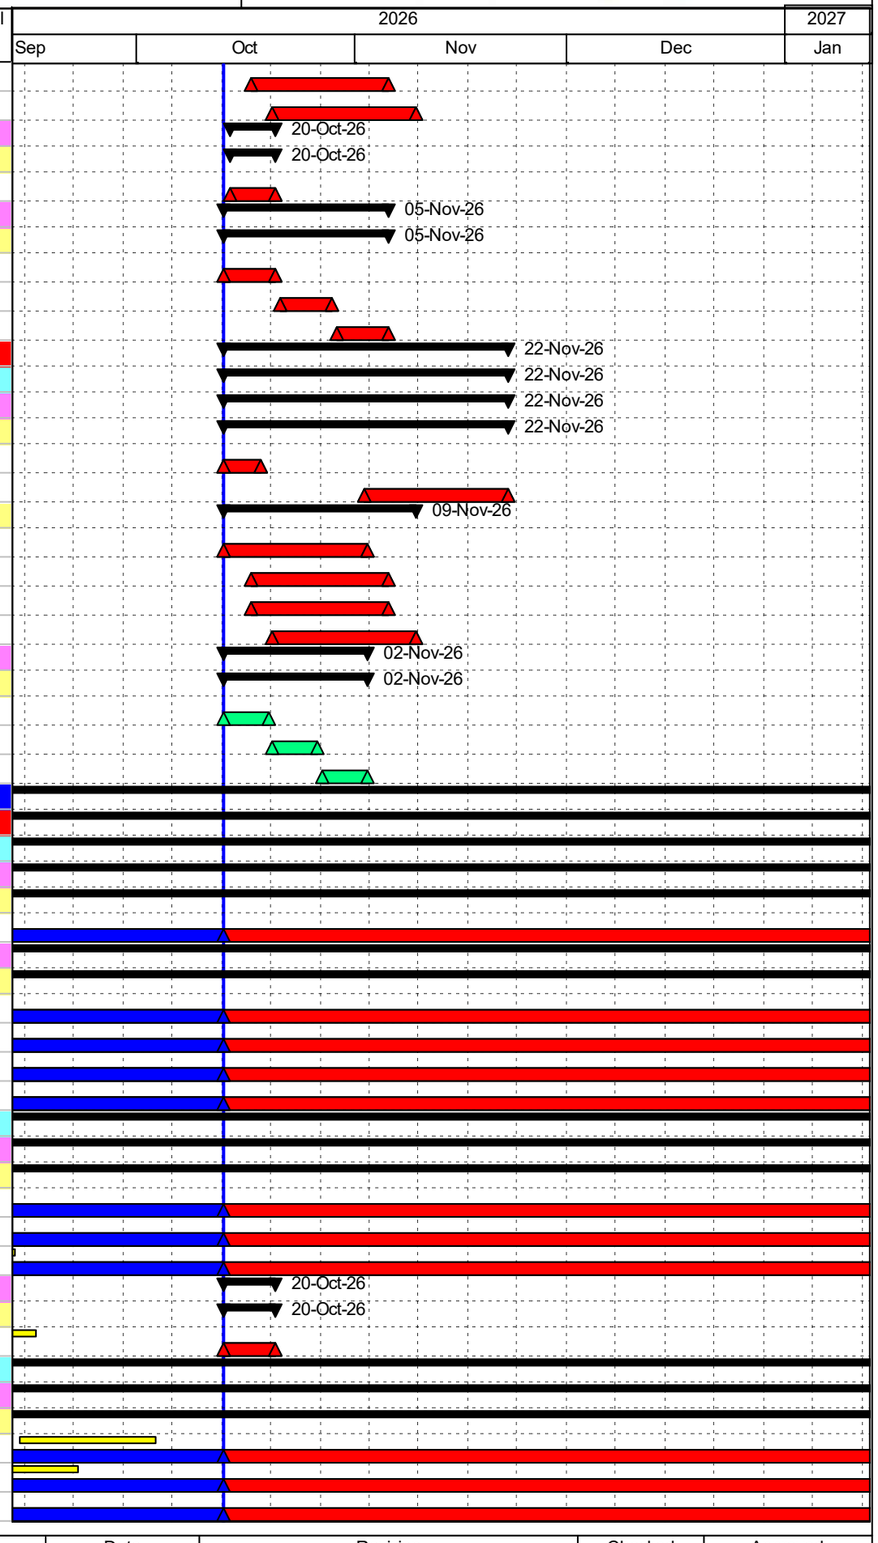


Primary Baseline | Actual Work | Summary
Remaining Work | Baseline Milestone
Critical Remaining Work | Milestone

Date	Revision	Checked	Approved
13-Oct-26	Third Industrial City		

Infrastructure Works of Area J -3rd Industrial City-
Dammam-Phase 2 - Update 13-10-2026
3Week Lookahead Schedule

Activity ID	Activity Name	Original Duration	Start	Finish	BL Project Start	BL Project Finish	Budgeted Total Cost
Independent Works		180	16-Sep-26 A	16-Nov-26	15-Feb-26	09-May-26	72,714
Sewage Pump Stations		30	16-Sep-26 A	16-Nov-26	05-Apr-26	09-May-26	66,973
Sewage Pump Station (PS 06)		30	16-Sep-26 A	16-Nov-26	05-Apr-26	09-May-26	66,973
Pump Station Main Building		30	16-Sep-26 A	16-Nov-26	05-Apr-26	09-May-26	66,973
CO-SW-PS7-MB-11	Concrete Works of Superstrucure	30	16-Sep-26 A	16-Nov-26	05-Apr-26	09-May-26	66,973
Storm Drainage Ponds		21	13-Oct-26	05-Nov-26	15-Feb-26	10-Mar-26	5,741
Storm Drainage Pond (PO-J1)		21	13-Oct-26	05-Nov-26	15-Feb-26	10-Mar-26	5,741
CO-SD-PO-K1-110-P	Finished Grouted Riprap - PART 1	21	13-Oct-26	05-Nov-26	15-Feb-26	10-Mar-26	5,741
Testing and Comissioning		50	01-Jun-26 A	06-Dec-27	07-Nov-26	03-Jan-27	11,075,669
Infrastructure Networks		50	01-Jun-26 A	06-Dec-27	07-Nov-26	03-Jan-27	11,075,669
Irrigation Network		12	05-Jun-26 A	05-Aug-27	12-Nov-26	25-Nov-26	624,274
T/C-IR	Testing and Commissioning of Irrigation Network	12	05-Jun-26 A	05-Aug-27	12-Nov-26	25-Nov-26	624,274
Potable Water Network		12	01-Jul-26 A	18-Oct-27	03-Dec-26	16-Dec-26	1,022,094
T/C-PW	Testing and Commissioning of Potable Water Network	12	01-Jul-26 A	18-Oct-27	03-Dec-26	16-Dec-26	1,022,094
Sewage Network		12	01-Jun-26 A	07-Oct-27	19-Dec-26	31-Dec-26	2,308,897
T/C-SW	Testing and Commissioning of Sewage Network	12	01-Jun-26 A	07-Oct-27	19-Dec-26	31-Dec-26	2,308,897
Storm Drainage Network		10	10-Jun-26 A	09-Sep-27	21-Dec-26	31-Dec-26	2,866,651
T/C-SD	Testing and Commissioning of Storm Drainage Network	10	10-Jun-26 A	09-Sep-27	21-Dec-26	31-Dec-26	2,866,651
Street Lighting Network		18	05-Sep-26 A	24-Oct-27	07-Nov-26	26-Nov-26	462,378
T/C-SL	Testing and Commissioning of Street Lighting Network	18	05-Sep-26 A	24-Oct-27	07-Nov-26	26-Nov-26	462,378
Telecom Network		10	05-Sep-26 A	06-Sep-27	10-Nov-26	21-Nov-26	181,657
T/C-TE	Testing and Commissioning of Telecom Network	10	05-Sep-26 A	06-Sep-27	10-Nov-26	21-Nov-26	181,657
Medium Voltage Network		10	05-Sep-26 A	06-Sep-27	22-Nov-26	02-Dec-26	478,905
T/C-MV	Testing and Commissioning of Medium Voltage Network	10	05-Sep-26 A	06-Sep-27	22-Nov-26	02-Dec-26	478,905
Road Works		5	16-Aug-26 A	06-Dec-27	29-Dec-26	03-Jan-27	3,130,812
T/C-RD	Testing and Commissioning of Road Works	5	16-Aug-26 A	06-Dec-27	29-Dec-26	03-Jan-27	3,130,812

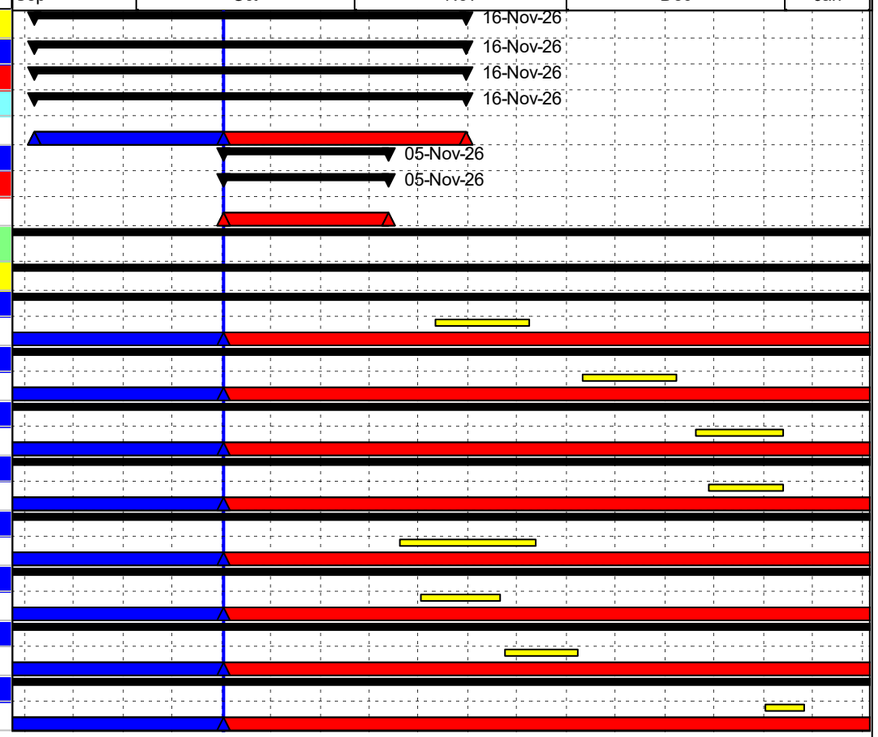

Primary Baseline
Remaining Work
Critical Remaining Work
Actual Work
Baseline Milestone
Milestone
Summary

Date	Revision	Checked	Approved
13-Oct-26	Third Industrial City		
