
Infrastructure Works of Area J -3rd Industrial City-Dammam-Phase 2 - Update 13-10-2026

Remaining work

Activity ID	Activity Name	Original Duration	Start	Finish	BL Project Start	BL Project Finish	Performance % Complete	Budgeted Total Cost	Remaining Total Cost
Infrastructure Works of Area J -3rd Industrial City-Dammam-Phase 2 - U		738	29-Oct-25 A	20-Dec-27	19-Mar-25	11-Jan-27	34.69%	44,915,753	44,184,281
Key Milestones		309	14-Dec-26	20-Dec-27	14-Feb-26	11-Jan-27	0%	0	0
Contractual Milestones		227	23-Mar-27	20-Dec-27	01-Sep-26	11-Jan-27	0%	0	0
MS-CF-MV	Completion of Construction Works for Medium Voltage Network	0		23-Mar-27*		28-Oct-26	0%	0	0
MS-CF-TE	Completion of Construction Works for Telecom Network	0		10-May-27*		01-Sep-26	0%	0	0
MS-CF-IR	Completion of Construction Works for Irrigation Network	0		22-Jul-27*		28-Oct-26	0%	0	0
MS-CF-SW	Completion of Construction Works for Sewage Network	0		12-Aug-27*		08-Nov-26	0%	0	0
MS-CF-SD	Completion of Construction Works for Storm Drainage Network	0		01-Sep-27*		12-Dec-26	0%	0	0
MS-CF-SL	Completion of Construction Works for Street Lighting Network	0		03-Oct-27*		15-Oct-26	0%	0	0
MS-CF-PW	Completion of Construction Works for Potable Water Network	0		04-Oct-27*		18-Nov-26	0%	0	0
MS-CF-RD	Completion of Construction Works for Road Works	0		06-Dec-27		28-Dec-26	0%	0	0
MS-CF-PF	Project Completion Date	0		20-Dec-27		11-Jan-27	0%	0	0
Control Milestones		0	14-Dec-26	14-Dec-26	14-Feb-26	14-Feb-26	0%	0	0
MS-CS-MV	The Employer Approval NOC for Medium Voltage Network	0	14-Dec-26		14-Feb-26		0%	0	0
Intermediate Milestones		148	15-Jun-27	06-Dec-27	24-Aug-26	28-Dec-26	0%	0	0
MS-MO-10	Completion of Sewage Pump Stations	0		15-Jun-27		01-Dec-26	0%	0	0
MS-MO-20	Completion of Storm Drainage Ponds	0		02-Aug-27		24-Aug-26	0%	0	0
MS-MO-30	Completion of Tie In To Existing Networks	0		06-Dec-27		28-Dec-26	0%	0	0
Procurement Cycle		612	29-Oct-25 A	29-Jul-27	03-May-25	05-Oct-26	38.78%	4,070,715	4,070,715
Short Lead Time Items		612	29-Oct-25 A	29-Jul-27	03-May-25	05-Oct-26	38.37%	3,034,811	3,034,811
Infrastructure Networks		612	13-Dec-25 A	29-Jul-27	03-May-25	05-Oct-26	24.53%	2,441,138	2,441,138
Road Works		240	13-Oct-26	29-Jul-27	20-Jul-25	05-Oct-26	0%	1,332,032	1,332,032
1st Material Delivery & Site Inspection		6	13-Oct-26	19-Oct-26	20-Jul-25	18-Aug-25	0%	0	0
Pavement Works		6	13-Oct-26	19-Oct-26	20-Jul-25	26-Jul-25	0%	0	0
PRO-RD-1DL-140	1ST Material Delivery for Interlock Tiles of Landscaping	6	13-Oct-26	19-Oct-26	20-Jul-25	26-Jul-25	0%	0	0
PRO-RD-1DL-150	1ST Material Delivery for Curbstones of Landscaping	6	13-Oct-26	19-Oct-26	20-Jul-25	26-Jul-25	0%	0	0
Traffic Signs Boards and Roads Marking		6	13-Oct-26	19-Oct-26	12-Aug-25	18-Aug-25	0%	0	0
PRO-RD-1DL-160	1ST Material Delivery for Traffic Signs Boards of Road Works	6	13-Oct-26	19-Oct-26	12-Aug-25	18-Aug-25	0%	0	0
PRO-RD-1DL-170	1ST Material Delivery for Road Markings of Road Works	6	13-Oct-26	19-Oct-26	12-Aug-25	18-Aug-25	0%	0	0
Material Delivery & Site Inspection		240	13-Oct-26	29-Jul-27	28-Dec-25	05-Oct-26	0%	1,332,032	1,332,032
Road 18 Local 1 (479 LM)		52	20-Oct-26	19-Dec-26	28-Dec-25	25-Feb-26	0%	6,300	6,300
Traffic Signs Boards and Roads Marking		52	20-Oct-26	19-Dec-26	28-Dec-25	25-Feb-26	0%	6,300	6,300
PRO-R18-RD-DL-	Material Delivery & Site Inspection of Traffic Signs Boards For Road Works	26	20-Oct-26	18-Nov-26	28-Dec-25	26-Jan-26	0%	1,971	1,971
PRO-R18-RD-DL-	Material Delivery & Site Inspection of Road Markings For Road Works	26	19-Nov-26	19-Dec-26	27-Jan-26	25-Feb-26	0%	4,329	4,329
Road 17 Local 1 (500 LM)		52	19-Nov-26	18-Jan-27	27-Jan-26	31-Mar-26	0%	5,981	5,981
Traffic Signs Boards and Roads Marking		52	19-Nov-26	18-Jan-27	27-Jan-26	31-Mar-26	0%	5,981	5,981
PRO-R17-RD-DL-	Material Delivery & Site Inspection of Traffic Signs Boards For Road Works	26	19-Nov-26	19-Dec-26	27-Jan-26	25-Feb-26	0%	1,505	1,505
PRO-R17-RD-DL-	Material Delivery & Site Inspection of Road Markings For Road Works	26	20-Dec-26	18-Jan-27	26-Feb-26	31-Mar-26	0%	4,476	4,476
Road 16 Local 1 (527 LM)		52	20-Dec-26	17-Feb-27	26-Feb-26	30-Apr-26	0%	6,736	6,736
Traffic Signs Boards and Roads Marking		52	20-Dec-26	17-Feb-27	26-Feb-26	30-Apr-26	0%	6,736	6,736
PRO-R16-RD-DL-	Material Delivery & Site Inspection of Traffic Signs Boards For Road Works	26	20-Dec-26	18-Jan-27	26-Feb-26	31-Mar-26	0%	2,028	2,028
PRO-R16-RD-DL-	Material Delivery & Site Inspection of Road Markings For Road Works	26	19-Jan-27	17-Feb-27	01-Apr-26	30-Apr-26	0%	4,708	4,708
Road 15 Local 1 (556 LM)		52	19-Jan-27	24-Mar-27	01-Apr-26	04-Jun-26	0%	7,173	7,173
Traffic Signs Boards and Roads Marking		52	19-Jan-27	24-Mar-27	01-Apr-26	04-Jun-26	0%	7,173	7,173
PRO-R15-RD-DL-	Material Delivery & Site Inspection of Traffic Signs Boards For Road Works	26	19-Jan-27	17-Feb-27	01-Apr-26	30-Apr-26	0%	2,233	2,233
PRO-R15-RD-DL-	Material Delivery & Site Inspection of Road Markings For Road Works	26	18-Feb-27	24-Mar-27	02-May-26	04-Jun-26	0%	4,940	4,940
Road 10 Local 2 (2352 LM)		162	13-Oct-26	24-Apr-27	26-Feb-26	05-Jul-26	0%	643,853	643,853
Bituminous Construction		26	13-Oct-26	11-Nov-26	26-Feb-26	30-Apr-26	0%	616,209	616,209
PRO-R10-RD-DL-	Material Delivery & Site Inspection for Prime Coat of Road Works	26	13-Oct-26	11-Nov-26	26-Feb-26	31-Mar-26	0%	123,243	123,243
PRO-R10-RD-DL-1	Material Delivery & Site Inspection for Bituminous Base & Wearing Courses of Road Works	26	13-Oct-26	11-Nov-26	01-Apr-26	30-Apr-26	0%	492,966	492,966

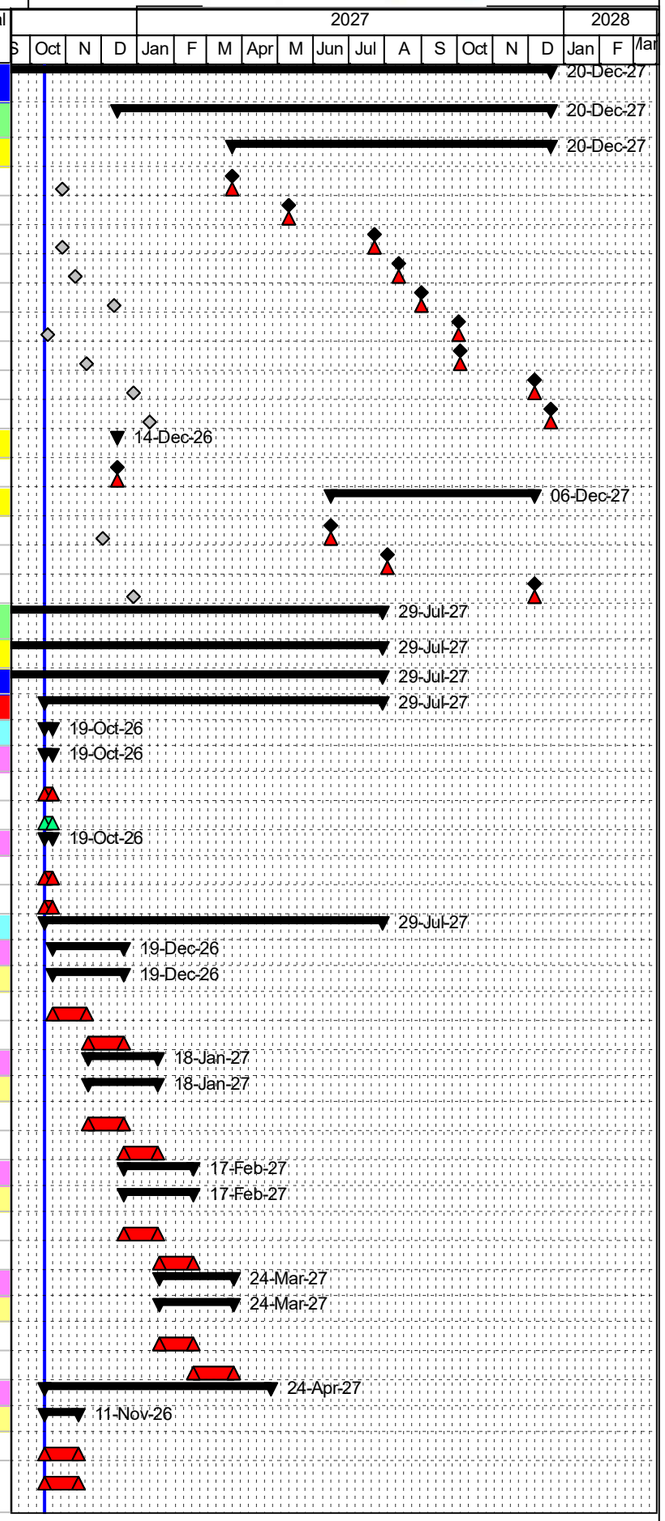

Primary Baseline | Actual Work | Summary


Remaining Work | Baseline Milestone

Critical Remaining Work | Milestone

Date	Revision	Checked	Approved
13-Oct-26	Third Industrial City		

Infrastructure Works of Area J -3rd Industrial City-
Dammam-Phase 2 - Update 13-10-2026
Remaining work


Activity ID	Activity Name	Original Duration	Start	Finish	BL Project Start	BL Project Finish	Performance % Complete	Budgeted Total Cost	Remaining Total Cost
Traffic Signs Boards and Roads Marking		52	18-Feb-27	24-Apr-27	02-May-26	05-Jul-26	0%	27,645	27,645
PRO-R10-RD-DL-	Material Delivery & Site Inspection of Traffic Signs Boards For Road Works	26	18-Feb-27	24-Mar-27	02-May-26	04-Jun-26	0%	7,533	7,533
PRO-R10-RD-DL-	Material Delivery & Site Inspection of Road Markings For Road Works	26	25-Mar-27	24-Apr-27	06-Jun-26	05-Jul-26	0%	20,112	20,112
Road 14 Local 1 (584 LM)		52	25-Mar-27	30-May-27	06-Jun-26	04-Aug-26	0%	12,022	12,022
Traffic Signs Boards and Roads Marking		52	25-Mar-27	30-May-27	06-Jun-26	04-Aug-26	0%	12,022	12,022
PRO-R14-RD-DL-	Material Delivery & Site Inspection of Traffic Signs Boards For Road Works	26	25-Mar-27	24-Apr-27	06-Jun-26	05-Jul-26	0%	3,362	3,362
PRO-R14-RD-DL-	Material Delivery & Site Inspection of Road Markings For Road Works	26	25-Apr-27	30-May-27	06-Jul-26	04-Aug-26	0%	8,661	8,661
Road 09 Local 2 (2278 LM)		214	13-Oct-26	29-Jun-27	02-May-26	03-Sep-26	0%	642,011	642,011
Bituminous Construction		26	13-Oct-26	11-Nov-26	02-May-26	05-Jul-26	0%	614,480	614,480
PRO-R09-RD-DL-	Material Delivery & Site Inspection for Prime Coat of Road Works	26	13-Oct-26	11-Nov-26	02-May-26	04-Jun-26	0%	122,896	122,896
PRO-R09-RD-DL-1	Material Delivery & Site Inspection for Bituminous Base & Wearing Courses of Road Works	26	13-Oct-26	11-Nov-26	06-Jun-26	05-Jul-26	0%	491,584	491,584
Traffic Signs Boards and Roads Marking		52	25-Apr-27	29-Jun-27	06-Jul-26	03-Sep-26	0%	27,531	27,531
PRO-R09-RD-DL-	Material Delivery & Site Inspection of Traffic Signs Boards For Road Works	26	25-Apr-27	30-May-27	06-Jul-26	04-Aug-26	0%	7,476	7,476
PRO-R09-RD-DL-	Material Delivery & Site Inspection of Road Markings For Road Works	26	31-May-27	29-Jun-27	05-Aug-26	03-Sep-26	0%	20,056	20,056
Road 11 Local 1 (670 LM)		52	31-May-27	29-Jul-27	05-Aug-26	05-Oct-26	0%	7,954	7,954
Traffic Signs Boards and Roads Marking		52	31-May-27	29-Jul-27	05-Aug-26	05-Oct-26	0%	7,954	7,954
PRO-R11-RD-DL-	Material Delivery & Site Inspection of Traffic Signs Boards For Road Works	26	31-May-27	29-Jun-27	05-Aug-26	03-Sep-26	0%	2,086	2,086
PRO-R11-RD-DL-	Material Delivery & Site Inspection of Road Markings For Road Works	26	30-Jun-27	29-Jul-27	05-Sep-26	05-Oct-26	0%	5,869	5,869
Sewage Network		156	13-Oct-26	17-Apr-27	26-Jul-25	29-Mar-26	0%	0	0
Material Delivery & Site Inspection		156	13-Oct-26	17-Apr-27	26-Jul-25	29-Mar-26	0%	0	0
Road 17 Local 1 (500 LM)		26	13-Oct-26	11-Nov-26	25-Aug-25	25-Oct-25	0%	0	0
Testing and Finishes		26	13-Oct-26	11-Nov-26	25-Aug-25	25-Oct-25	0%	0	0
PRO-R17-SW-DL-	Material Delivery & Site Inspection of Manholes Covers for Sewage Network	26	13-Oct-26	11-Nov-26	25-Aug-25	24-Sep-25	0%	0	0
PRO-R17-SW-DL-	Material Delivery & Site Inspection of Membrane Insulation for Sewage Networl	26	13-Oct-26	11-Nov-26	25-Sep-25	25-Oct-25	0%	0	0
Road 16 Local 1 (527 LM)		26	12-Nov-26	12-Dec-26	25-Sep-25	24-Nov-25	0%	0	0
Testing and Finishes		26	12-Nov-26	12-Dec-26	25-Sep-25	24-Nov-25	0%	0	0
PRO-R16-SW-DL-	Material Delivery & Site Inspection of Manholes Covers for Sewage Network	26	12-Nov-26	12-Dec-26	25-Sep-25	25-Oct-25	0%	0	0
PRO-R16-SW-DL-	Material Delivery & Site Inspection of Membrane Insulation for Sewage Networl	26	12-Nov-26	12-Dec-26	26-Oct-25	24-Nov-25	0%	0	0
Road 15 Local 1 (556 LM)		26	13-Dec-26	11-Jan-27	26-Oct-25	24-Dec-25	0%	0	0
Testing and Finishes		26	13-Dec-26	11-Jan-27	26-Oct-25	24-Dec-25	0%	0	0
PRO-R15-SW-DL-	Material Delivery & Site Inspection of Manholes Covers for Sewage Network	26	13-Dec-26	11-Jan-27	26-Oct-25	24-Nov-25	0%	0	0
PRO-R15-SW-DL-	Material Delivery & Site Inspection of Membrane Insulation for Sewage Networl	26	13-Dec-26	11-Jan-27	25-Nov-25	24-Dec-25	0%	0	0
Road 10 Local 2 (2352 LM)		26	12-Jan-27	10-Feb-27	25-Nov-25	24-Jan-26	0%	0	0
Testing and Finishes		26	12-Jan-27	10-Feb-27	25-Nov-25	24-Jan-26	0%	0	0
PRO-R10-SW-DL-	Material Delivery & Site Inspection of Manholes Covers for Sewage Network	26	12-Jan-27	10-Feb-27	25-Nov-25	24-Dec-25	0%	0	0
PRO-R10-SW-DL-	Material Delivery & Site Inspection of Membrane Insulation for Sewage Networl	26	12-Jan-27	10-Feb-27	25-Dec-25	24-Jan-26	0%	0	0
Road 14 Local 1 (584 LM)		26	11-Feb-27	17-Mar-27	25-Dec-25	23-Feb-26	0%	0	0
Testing and Finishes		26	11-Feb-27	17-Mar-27	25-Dec-25	23-Feb-26	0%	0	0
PRO-R14-SW-DL-	Material Delivery & Site Inspection of Manholes Covers for Sewage Network	26	11-Feb-27	17-Mar-27	25-Dec-25	24-Jan-26	0%	0	0
PRO-R14-SW-DL-	Material Delivery & Site Inspection of Membrane Insulation for Sewage Networl	26	11-Feb-27	17-Mar-27	25-Jan-26	23-Feb-26	0%	0	0
Road 09 Local 2 (2278 LM)		38	13-Oct-26	25-Nov-26	26-Jul-25	07-Sep-25	0%	0	0
Testing and Finishes		38	13-Oct-26	25-Nov-26	26-Jul-25	07-Sep-25	0%	0	0
PRO-R09-SW-DL-	Material Delivery & Site Inspection of Manholes Covers for Rising Main Networl	38	13-Oct-26	25-Nov-26	26-Jul-25	07-Sep-25	0%	0	0
PRO-R09-SW-DL-1	Material Delivery & Site Inspection of Membrane Insulation for Rising Main Network	38	13-Oct-26	25-Nov-26	26-Jul-25	07-Sep-25	0%	0	0
Road 11 Local 1 (670 LM)		26	18-Mar-27	17-Apr-27	25-Jan-26	29-Mar-26	0%	0	0
Testing and Finishes		26	18-Mar-27	17-Apr-27	25-Jan-26	29-Mar-26	0%	0	0
PRO-R11-SW-DL-	Material Delivery & Site Inspection of Manholes Covers for Sewage Network	26	18-Mar-27	17-Apr-27	25-Jan-26	23-Feb-26	0%	0	0
PRO-R11-SW-DL-	Material Delivery & Site Inspection of Membrane Insulation for Sewage Networl	26	18-Mar-27	17-Apr-27	24-Feb-26	29-Mar-26	0%	0	0
Storm Drainage Network		538	20-Jun-26 A	28-Apr-27	26-Jul-25	29-Mar-26	0%	0	0
Material Delivery & Site Inspection		538	20-Jun-26 A	28-Apr-27	26-Jul-25	29-Mar-26	0%	0	0
Road 18 Local 1 (479 LM)		26	27-Jun-26 A	24-Oct-26	26-Jul-25	24-Aug-25	0%	0	0
Testing and Finishes		26	27-Jun-26 A	24-Oct-26	26-Jul-25	24-Aug-25	0%	0	0

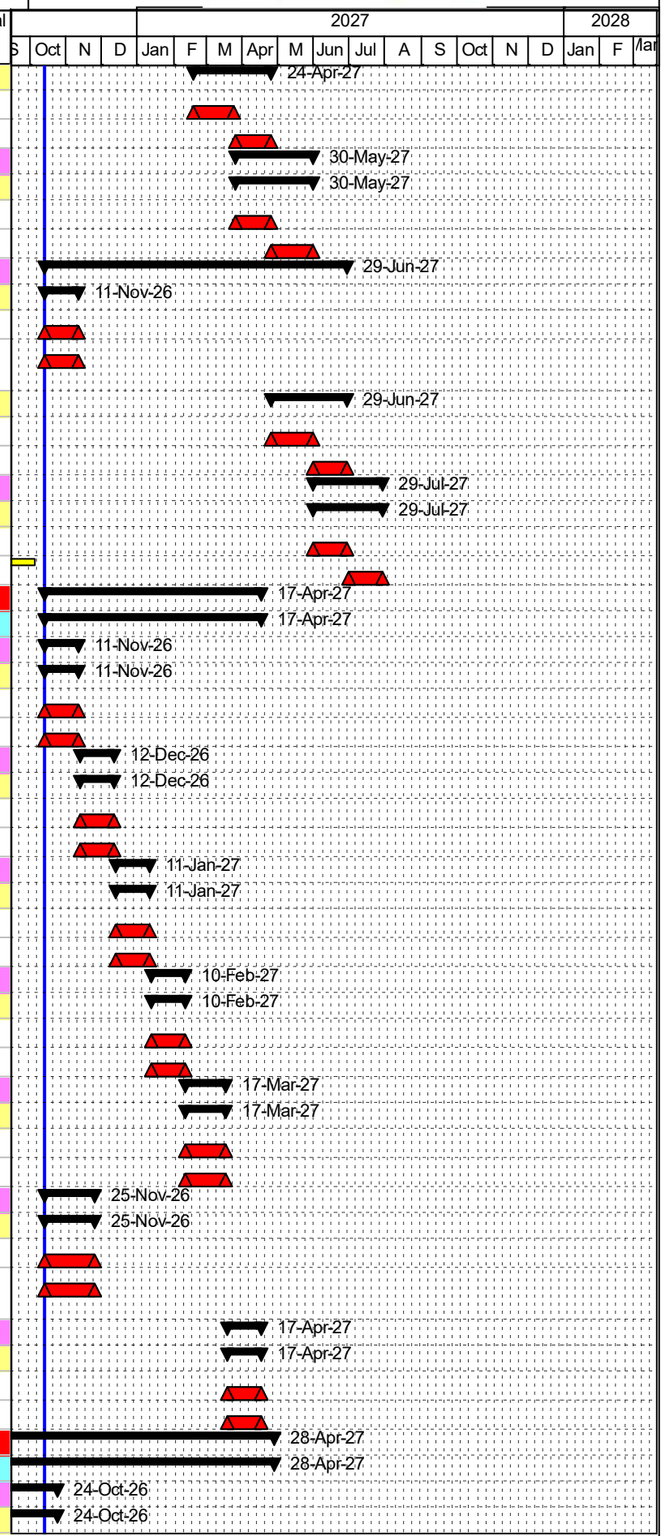

Primary Baseline | Actual Work | Summary
Remaining Work | Baseline Milestone
Critical Remaining Work | Milestone

Date	Revision	Checked	Approved
13-Oct-26	Third Industrial City		


Activity ID	Activity Name	Original Duration	Start	Finish	BL Project Start	BL Project Finish	Performance % Complete	Budgeted Total Cost	Remaining Total Cost
PRO-R18-SD-DL-19	Material Delivery & Site Inspection of Manholes Covers for Storm Drainage Network	26	27-Jun-26 A	24-Oct-26	26-Jul-25	24-Aug-25	0%	0	0
PRO-R18-SD-DL-21	Material Delivery & Site Inspection of Catch Basin Covers for Storm Drainage Network	26	27-Jun-26 A	24-Oct-26	26-Jul-25	24-Aug-25	0%	0	0
PRO-R18-SD-DL-23	Material Delivery & Site Inspection of Epoxy Insulation for Storm Drainage Network	26	27-Jun-26 A	24-Oct-26	26-Jul-25	24-Aug-25	0%	0	0
Road 17 Local 1 (500 LM)		26	20-Jun-26 A	24-Oct-26	25-Aug-25	24-Sep-25	0%	0	0
Testing and Finishes		26	20-Jun-26 A	24-Oct-26	25-Aug-25	24-Sep-25	0%	0	0
PRO-R17-SD-DL-14	Material Delivery & Site Inspection of Manholes Covers for Storm Drainage Network	26	20-Jun-26 A	24-Oct-26	25-Aug-25	24-Sep-25	0%	0	0
PRO-R17-SD-DL-15	Material Delivery & Site Inspection of Catch Basin Covers for Storm Drainage Network	26	20-Jun-26 A	24-Oct-26	25-Aug-25	24-Sep-25	0%	0	0
PRO-R17-SD-DL-16	Material Delivery & Site Inspection of Epoxy Insulation for Storm Drainage Network	26	20-Jun-26 A	24-Oct-26	25-Aug-25	24-Sep-25	0%	0	0
Road 16 Local 1 (527 LM)		26	25-Oct-26	23-Nov-26	25-Sep-25	25-Oct-25	0%	0	0
Testing and Finishes		26	25-Oct-26	23-Nov-26	25-Sep-25	25-Oct-25	0%	0	0
PRO-R16-SD-DL-14	Material Delivery & Site Inspection of Manholes Covers for Storm Drainage Network	26	25-Oct-26	23-Nov-26	25-Sep-25	25-Oct-25	0%	0	0
PRO-R16-SD-DL-15	Material Delivery & Site Inspection of Catch Basin Covers for Storm Drainage Network	26	25-Oct-26	23-Nov-26	25-Sep-25	25-Oct-25	0%	0	0
PRO-R16-SD-DL-16	Material Delivery & Site Inspection of Epoxy Insulation for Storm Drainage Network	26	25-Oct-26	23-Nov-26	25-Sep-25	25-Oct-25	0%	0	0
Road 15 Local 1 (556 LM)		26	24-Nov-26	23-Dec-26	26-Oct-25	24-Nov-25	0%	0	0
Testing and Finishes		26	24-Nov-26	23-Dec-26	26-Oct-25	24-Nov-25	0%	0	0
PRO-R15-SD-DL-14	Material Delivery & Site Inspection of Manholes Covers for Storm Drainage Network	26	24-Nov-26	23-Dec-26	26-Oct-25	24-Nov-25	0%	0	0
PRO-R15-SD-DL-15	Material Delivery & Site Inspection of Catch Basin Covers for Storm Drainage Network	26	24-Nov-26	23-Dec-26	26-Oct-25	24-Nov-25	0%	0	0
PRO-R15-SD-DL-16	Material Delivery & Site Inspection of Epoxy Insulation for Storm Drainage Network	26	24-Nov-26	23-Dec-26	26-Oct-25	24-Nov-25	0%	0	0
Road 10 Local 2 (2352 LM)		26	24-Dec-26	23-Jan-27	25-Nov-25	24-Dec-25	0%	0	0
Testing and Finishes		26	24-Dec-26	23-Jan-27	25-Nov-25	24-Dec-25	0%	0	0
PRO-R10-SD-DL-14	Material Delivery & Site Inspection of Manholes Covers for Storm Drainage Network	26	24-Dec-26	23-Jan-27	25-Nov-25	24-Dec-25	0%	0	0
PRO-R10-SD-DL-15	Material Delivery & Site Inspection of Catch Basin Covers for Storm Drainage Network	26	24-Dec-26	23-Jan-27	25-Nov-25	24-Dec-25	0%	0	0
PRO-R10-SD-DL-16	Material Delivery & Site Inspection of Epoxy Insulation for Storm Drainage Network	26	24-Dec-26	23-Jan-27	25-Nov-25	24-Dec-25	0%	0	0
Road 14 Local 1 (584 LM)		26	24-Jan-27	23-Feb-27	25-Dec-25	24-Jan-26	0%	0	0
Testing and Finishes		26	24-Jan-27	23-Feb-27	25-Dec-25	24-Jan-26	0%	0	0
PRO-R14-SD-DL-14	Material Delivery & Site Inspection of Manholes Covers for Storm Drainage Network	26	24-Jan-27	23-Feb-27	25-Dec-25	24-Jan-26	0%	0	0
PRO-R14-SD-DL-15	Material Delivery & Site Inspection of Catch Basin Covers for Storm Drainage Network	26	24-Jan-27	23-Feb-27	25-Dec-25	24-Jan-26	0%	0	0
PRO-R14-SD-DL-16	Material Delivery & Site Inspection of Epoxy Insulation for Storm Drainage Network	26	24-Jan-27	23-Feb-27	25-Dec-25	24-Jan-26	0%	0	0
Road 09 Local 2 (2278 LM)		26	24-Feb-27	29-Mar-27	25-Jan-26	23-Feb-26	0%	0	0
Testing and Finishes		26	24-Feb-27	29-Mar-27	25-Jan-26	23-Feb-26	0%	0	0
PRO-R09-SD-DL-14	Material Delivery & Site Inspection of Manholes Covers for Storm Drainage Network	26	24-Feb-27	29-Mar-27	25-Jan-26	23-Feb-26	0%	0	0
PRO-R09-SD-DL-15	Material Delivery & Site Inspection of Catch Basin Covers for Storm Drainage Network	26	24-Feb-27	29-Mar-27	25-Jan-26	23-Feb-26	0%	0	0
PRO-R09-SD-DL-16	Material Delivery & Site Inspection of Epoxy Insulation for Storm Drainage Network	26	24-Feb-27	29-Mar-27	25-Jan-26	23-Feb-26	0%	0	0
Road 11 Local 1 (670 LM)		26	30-Mar-27	28-Apr-27	24-Feb-26	29-Mar-26	0%	0	0
Testing and Finishes		26	30-Mar-27	28-Apr-27	24-Feb-26	29-Mar-26	0%	0	0

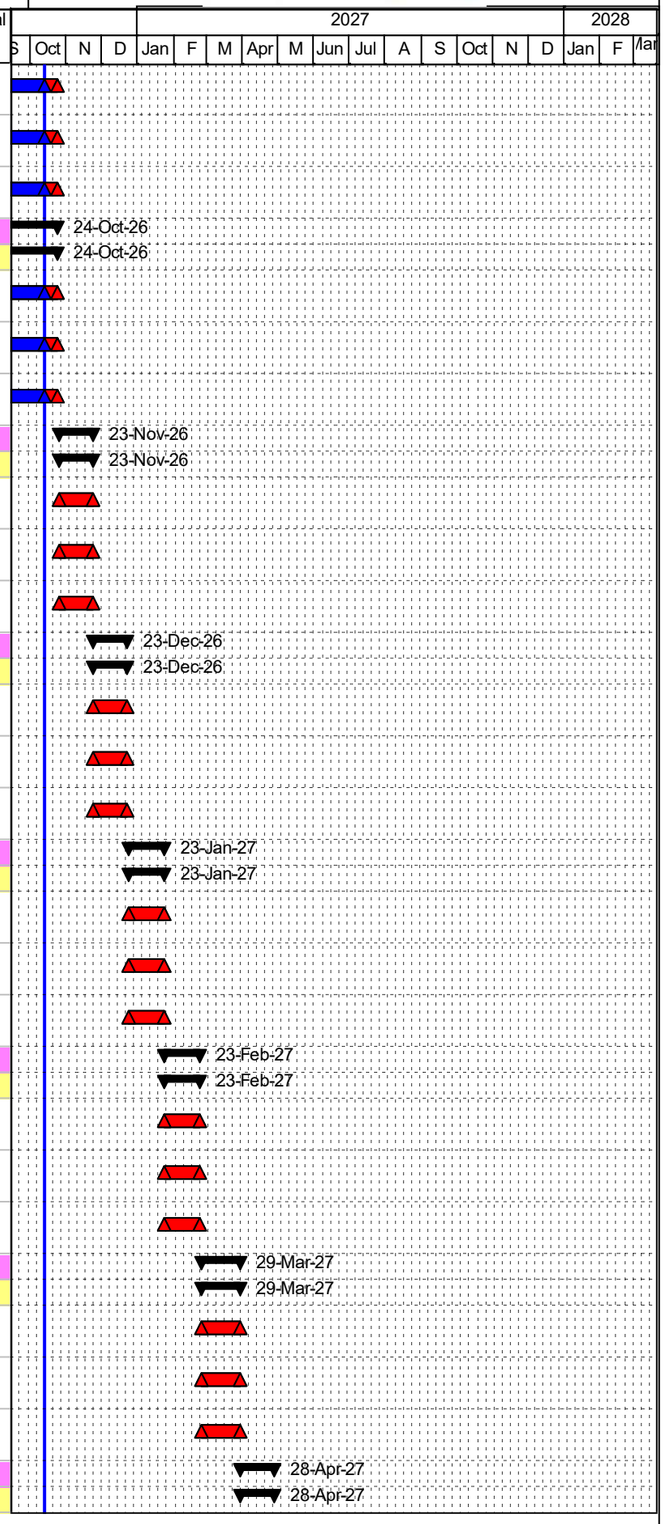

Primary Baseline
Actual Work
Summary
Remaining Work
Baseline Milestone
Critical Remaining Work
Milestone

Date	Revision	Checked	Approved
13-Oct-26	Third Industrial City		

Activity ID	Activity Name	Original Duration	Start	Finish	BL Project Start	BL Project Finish	Performance % Complete	Budgeted Total Cost	Remaining Total Cost
PRO-R11-SD-DL-14	Material Delivery & Site Inspection of Manholes Covers for Storm Drainage Network	26	30-Mar-27	28-Apr-27	24-Feb-26	29-Mar-26	0%	0	0
PRO-R11-SD-DL-15	Material Delivery & Site Inspection of Catch Basin Covers for Storm Drainage Network	26	30-Mar-27	28-Apr-27	24-Feb-26	29-Mar-26	0%	0	0
PRO-R11-SD-DL-16	Material Delivery & Site Inspection of Epoxy Insulation for Storm Drainage Network	26	30-Mar-27	28-Apr-27	24-Feb-26	29-Mar-26	0%	0	0
Potable Water Network		484	13-Dec-25 A	17-Apr-27	31-May-25	09-Feb-26	36.91%	467,139	467,139
1st Material Delivery & Site Inspection		6	13-Oct-26	19-Oct-26	31-May-25	10-Jun-25	0%	0	0
Testing and Finishes		6	13-Oct-26	19-Oct-26	31-May-25	10-Jun-25	0%	0	0
PRO-PW-1DL-130	1ST Material Delivery for Finishes of Potable Water Network	6	13-Oct-26	19-Oct-26	31-May-25	10-Jun-25	0%	0	0
Material Delivery & Site Inspection		484	13-Dec-25 A	17-Apr-27	11-Jun-25	09-Feb-26	36.91%	467,139	467,139
Road 18 Local 1 (479 LM)		26	20-Oct-26	18-Nov-26	11-Jun-25	10-Jul-25	0%	0	0
Testing and Finishes		26	20-Oct-26	18-Nov-26	11-Jun-25	10-Jul-25	0%	0	0
PRO-R18-PW-DL-	Material Delivery & Site Inspection for Finishes of Potable Water Network	26	20-Oct-26	18-Nov-26	11-Jun-25	10-Jul-25	0%	0	0
Road 17 Local 1 (500 LM)		58	13-Oct-26	19-Dec-26	16-Jun-25	10-Aug-25	0%	5,533	5,533
Main Line Sections		26	13-Oct-26	11-Nov-26	16-Jun-25	15-Jul-25	0%	5,533	5,533
PRO-R17-PW-DL-	Material Delivery & Site Inspection of Valves for Potable Water Network	26	13-Oct-26	11-Nov-26	16-Jun-25	15-Jul-25	0%	5,533	5,533
Testing and Finishes		26	19-Nov-26	19-Dec-26	12-Jul-25	10-Aug-25	0%	0	0
PRO-R17-PW-DL-	Material Delivery & Site Inspection for Finishes of Potable Water Network	26	19-Nov-26	19-Dec-26	12-Jul-25	10-Aug-25	0%	0	0
Road 16 Local 1 (527 LM)		58	12-Nov-26	18-Jan-27	16-Jul-25	09-Sep-25	0%	3,952	3,952
Main Line Sections		26	12-Nov-26	12-Dec-26	16-Jul-25	14-Aug-25	0%	3,952	3,952
PRO-R16-PW-DL-	Material Delivery & Site Inspection of Valves for Potable Water Network	26	12-Nov-26	12-Dec-26	16-Jul-25	14-Aug-25	0%	3,952	3,952
Testing and Finishes		26	20-Dec-26	18-Jan-27	11-Aug-25	09-Sep-25	0%	0	0
PRO-R16-PW-DL-	Material Delivery & Site Inspection for Finishes of Potable Water Network	26	20-Dec-26	18-Jan-27	11-Aug-25	09-Sep-25	0%	0	0
Road 15 Local 1 (556 LM)		58	13-Dec-26	17-Feb-27	16-Aug-25	11-Oct-25	0%	4,742	4,742
Main Line Sections		26	13-Dec-26	11-Jan-27	16-Aug-25	14-Sep-25	0%	4,742	4,742
PRO-R15-PW-DL-	Material Delivery & Site Inspection of Valves for Potable Water Network	26	13-Dec-26	11-Jan-27	16-Aug-25	14-Sep-25	0%	4,742	4,742
Testing and Finishes		26	19-Jan-27	17-Feb-27	10-Sep-25	11-Oct-25	0%	0	0
PRO-R15-PW-DL-	Material Delivery & Site Inspection for Finishes of Potable Water Network	26	19-Jan-27	17-Feb-27	10-Sep-25	11-Oct-25	0%	0	0
Road 10 Local 2 (2352 LM)		464	13-Dec-25 A	24-Mar-27	15-Sep-25	10-Nov-25	60.95%	282,851	282,851
Main Line Sections		26	13-Dec-25 A	11-Jan-27	15-Sep-25	15-Oct-25	80%	215,514	215,514
PRO-R10-PW-DL-	Material Delivery & Site Inspection of Valves for Potable Water Network	26	13-Dec-25 A	11-Jan-27	15-Sep-25	15-Oct-25	80%	215,514	215,514
Testing and Finishes		26	18-Feb-27	24-Mar-27	12-Oct-25	10-Nov-25	0%	67,337	67,337
PRO-R10-PW-DL-	Material Delivery & Site Inspection for Finishes of Potable Water Network	26	18-Feb-27	24-Mar-27	12-Oct-25	10-Nov-25	0%	67,337	67,337
Road 14 Local 1 (584 LM)		26	12-Jan-27	10-Feb-27	16-Oct-25	15-Nov-25	0%	146,233	146,233
Main Line Sections		26	12-Jan-27	10-Feb-27	16-Oct-25	15-Nov-25	0%	146,233	146,233
PRO-R14-PW-DL-	Material Delivery & Site Inspection of Valves for Potable Water Network	26	12-Jan-27	10-Feb-27	16-Oct-25	15-Nov-25	0%	146,233	146,233
Road 09 Local 2 (2278 LM)		124	20-Oct-26	17-Mar-27	16-Nov-25	10-Jan-26	0%	19,085	19,085
Main Line Sections		26	11-Feb-27	17-Mar-27	16-Nov-25	15-Dec-25	0%	19,085	19,085
PRO-R09-PW-DL-	Material Delivery & Site Inspection of Valves for Potable Water Network	26	11-Feb-27	17-Mar-27	16-Nov-25	15-Dec-25	0%	19,085	19,085
Testing and Finishes		26	20-Oct-26	18-Nov-26	11-Dec-25	10-Jan-26	0%	0	0
PRO-R09-PW-DL-	Material Delivery & Site Inspection for Finishes of Potable Water Network	26	20-Oct-26	18-Nov-26	11-Dec-25	10-Jan-26	0%	0	0
Road 11 Local 1 (670 LM)		124	19-Nov-26	17-Apr-27	16-Dec-25	09-Feb-26	0%	4,742	4,742
Main Line Sections		26	18-Mar-27	17-Apr-27	16-Dec-25	14-Jan-26	0%	4,742	4,742
PRO-R11-PW-DL-	Material Delivery & Site Inspection of Valves for Potable Water Network	26	18-Mar-27	17-Apr-27	16-Dec-25	14-Jan-26	0%	4,742	4,742
Testing and Finishes		26	19-Nov-26	19-Dec-26	11-Jan-26	09-Feb-26	0%	0	0
PRO-R11-PW-DL-	Material Delivery & Site Inspection for Finishes of Potable Water Network	26	19-Nov-26	19-Dec-26	11-Jan-26	09-Feb-26	0%	0	0
Irrigation Network		70	13-Oct-26	02-Jan-27	17-Jul-25	07-Oct-25	0%	24,472	24,472
1st Material Delivery & Site Inspection		6	13-Oct-26	19-Oct-26	17-Jul-25	23-Jul-25	0%	0	0
Main Line Pipes		6	13-Oct-26	19-Oct-26	17-Jul-25	23-Jul-25	0%	0	0
PRO-IR-1DL-110	1ST Material Delivery for Valves of Irrigation Network	6	13-Oct-26	19-Oct-26	17-Jul-25	23-Jul-25	0%	0	0
Material Delivery & Site Inspection		64	20-Oct-26	02-Jan-27	24-Jul-25	07-Oct-25	0%	24,472	24,472
Road 18 Local 1 (479 LM)		16	20-Oct-26	07-Nov-26	24-Jul-25	11-Aug-25	0%	4,632	4,632
Main Line Pipes		16	20-Oct-26	07-Nov-26	24-Jul-25	11-Aug-25	0%	4,632	4,632

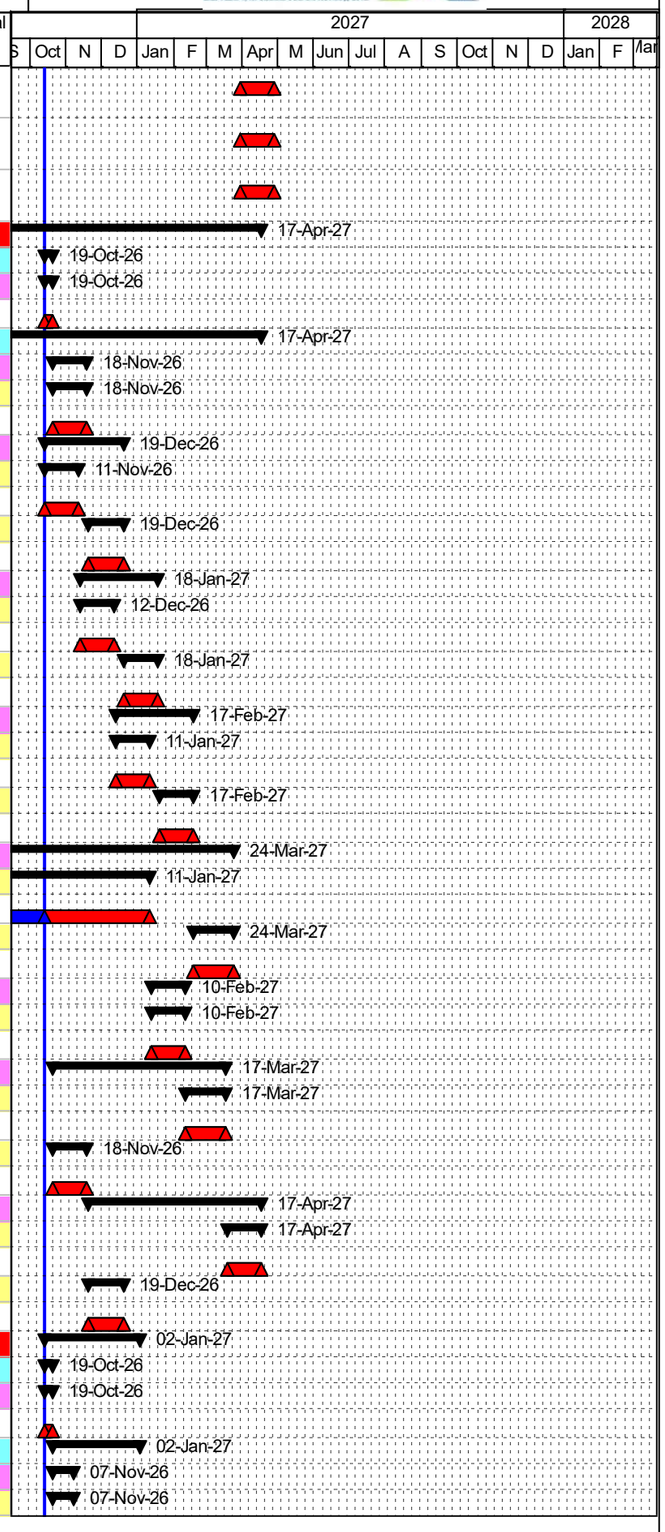


Primary Baseline
Remaining Work
Critical Remaining Work
Actual Work
Baseline Milestone
Milestone
Summary

Date	Revision	Checked	Approved
13-Oct-26	Third Industrial City		

Infrastructure Works of Area J -3rd Industrial City-
Dammam-Phase 2 - Update 13-10-2026
Remaining work


Activity ID	Activity Name	Original Duration	Start	Finish	BL Project Start	BL Project Finish	Performance % Complete	Budgeted Total Cost	Remaining Total Cost
PRO-R18-IR-DL-1	Material Delivery & Site Inspection of Valves for Irrigation Network	16	20-Oct-26	07-Nov-26	24-Jul-25	11-Aug-25	0%	4,632	4,632
Road 17 Local 1 (500 LM)		16	08-Nov-26	25-Nov-26	12-Aug-25	30-Aug-25	0%	10,795	10,795
Main Line Pipes		16	08-Nov-26	25-Nov-26	12-Aug-25	30-Aug-25	0%	10,795	10,795
PRO-R17-IR-DL-1	Material Delivery & Site Inspection of Valves for Irrigation Network	16	08-Nov-26	25-Nov-26	12-Aug-25	30-Aug-25	0%	10,795	10,795
Road 16 Local 1 (527 LM)		16	26-Nov-26	14-Dec-26	31-Aug-25	17-Sep-25	0%	5,475	5,475
Main Line Pipes		16	26-Nov-26	14-Dec-26	31-Aug-25	17-Sep-25	0%	5,475	5,475
PRO-R16-IR-DL-1	Material Delivery & Site Inspection of Valves for Irrigation Network	16	26-Nov-26	14-Dec-26	31-Aug-25	17-Sep-25	0%	5,475	5,475
Road 15 Local 1 (556 LM)		16	15-Dec-26	02-Jan-27	18-Sep-25	07-Oct-25	0%	3,570	3,570
Main Line Pipes		16	15-Dec-26	02-Jan-27	18-Sep-25	07-Oct-25	0%	3,570	3,570
PRO-R15-IR-DL-1	Material Delivery & Site Inspection of Valves for Irrigation Network	16	15-Dec-26	02-Jan-27	18-Sep-25	07-Oct-25	0%	3,570	3,570
Medium Voltage Network		350	13-Dec-25 A	11-Jan-27	03-May-25	19-Jan-26	90%	359,338	359,338
1st Material Delivery & Site Inspection		52	13-Oct-26	12-Dec-26	03-May-25	10-Nov-25	0%	0	0
RMU Concrete Works		52	13-Oct-26	12-Dec-26	10-Sep-25	10-Nov-25	0%	0	0
PRO-MV-1DL-110	1ST Material Delivery for RMU Concrete Foundations of Medium Voltage Network	52	13-Oct-26	12-Dec-26	10-Sep-25	10-Nov-25	0%	0	0
Termination and Testing Works		26	13-Oct-26	11-Nov-26	03-May-25	01-Jun-25	0%	0	0
PRO-MV-1DL-120	1ST Material Delivery for Termination and Joints Kits of Medium Voltage Network	26	13-Oct-26	11-Nov-26	03-May-25	01-Jun-25	0%	0	0
Material Delivery & Site Inspection		350	13-Dec-25 A	11-Jan-27	20-Nov-25	19-Jan-26	90%	359,338	359,338
Road 10 Local 2 (2352 LM)		26	13-Dec-26	11-Jan-27	21-Dec-25	19-Jan-26	0%	0	0
RMU Concrete Works		26	13-Dec-26	11-Jan-27	21-Dec-25	19-Jan-26	0%	0	0
PRO-R10-MV-DL-12	Material Delivery & Site Inspection of RMU Concrete Foundations for Medium Voltage Network	26	13-Dec-26	11-Jan-27	21-Dec-25	19-Jan-26	0%	0	0
Road 09 Local 2 (2278 LM)		26	13-Dec-25 A	11-Nov-26	20-Nov-25	20-Dec-25	90%	359,338	359,338
Cabling Works		26	13-Dec-25 A	11-Nov-26	20-Nov-25	20-Dec-25	90%	359,338	359,338
PRO-R09-MV-DL-1(	Material Delivery & Site Inspection of Medium Voltage Cables for Medium Voltage Network	26	13-Dec-25 A	11-Nov-26	20-Nov-25	20-Dec-25	90%	359,338	359,338
Street Lighting Network		606	21-Sep-26 A	29-Jul-27	26-Jul-25	23-Jun-26	39.9%	258,158	258,158
1st Material Delivery & Site Inspection		15	13-Oct-26	29-Oct-26	26-Jul-25	11-Aug-25	0%	0	0
Lighting Poles Works		6	13-Oct-26	19-Oct-26	26-Jul-25	31-Jul-25	0%	0	0
PRO-SL-1DL-140	1ST Material Delivery for Lighting Fixtures of Street Lighting Network	6	13-Oct-26	19-Oct-26	26-Jul-25	31-Jul-25	0%	0	0
Distribution Panel Board		6	13-Oct-26	19-Oct-26	26-Jul-25	31-Jul-25	0%	0	0
PRO-SL-1DL-160	1ST Material Delivery for Distrubution Panel Boards of Street Lighting Network	6	13-Oct-26	19-Oct-26	26-Jul-25	31-Jul-25	0%	0	0
Termination and Testing Works		15	13-Oct-26	29-Oct-26	26-Jul-25	11-Aug-25	0%	0	0
PRO-SL-1DL-130	1ST Material Delivery for Fuse Boxes of Street Lighting Network	15	13-Oct-26	29-Oct-26	26-Jul-25	11-Aug-25	0%	0	0
PRO-SL-1DL-170	1ST Material Delivery for Cable Lugs of Street Lighting Network	15	13-Oct-26	29-Oct-26	26-Jul-25	11-Aug-25	0%	0	0
Earthing System Works		6	13-Oct-26	19-Oct-26	26-Jul-25	31-Jul-25	0%	0	0
PRO-SL-1DL-150	1ST Material Delivery for Lighting Earthing of Street Lighting Network	6	13-Oct-26	19-Oct-26	26-Jul-25	31-Jul-25	0%	0	0
Material Delivery & Site Inspection		606	21-Sep-26 A	29-Jul-27	02-Aug-25	23-Jun-26	39.9%	258,158	258,158
Road 18 Local 1 (479 LM)		78	20-Oct-26	18-Jan-27	16-Aug-25	15-Nov-25	0%	8,512	8,512
Lighting Poles Works		26	20-Oct-26	18-Nov-26	16-Aug-25	14-Sep-25	0%	3,755	3,755
PRO-R18-SL-DL-22	Material Delivery & Site Inspection of Lighting Fixtures for Street Lighting Network	26	20-Oct-26	18-Nov-26	16-Aug-25	14-Sep-25	0%	3,755	3,755
Termination and Testing Works		52	19-Nov-26	18-Jan-27	15-Sep-25	15-Nov-25	0%	4,757	4,757
PRO-R18-SL-DL-2	Material Delivery & Site Inspection of Fuse Boxes for Street Lighting Network	26	19-Nov-26	19-Dec-26	15-Sep-25	15-Oct-25	0%	4,757	4,757
PRO-R18-SL-DL-2	Material Delivery & Site Inspection of Cable Lugs for Street Lighting Network	26	20-Dec-26	18-Jan-27	16-Oct-25	15-Nov-25	0%	0	0
Road 17 Local 1 (500 LM)		78	19-Nov-26	17-Feb-27	15-Sep-25	15-Dec-25	0%	8,014	8,014
Lighting Poles Works		26	19-Nov-26	19-Dec-26	15-Sep-25	15-Oct-25	0%	3,934	3,934
PRO-R17-SL-DL-14	Material Delivery & Site Inspection of Lighting Fixtures for Street Lighting Network	26	19-Nov-26	19-Dec-26	15-Sep-25	15-Oct-25	0%	3,934	3,934
Termination and Testing Works		52	20-Dec-26	17-Feb-27	16-Oct-25	15-Dec-25	0%	4,081	4,081
PRO-R17-SL-DL-	Material Delivery & Site Inspection of Fuse Boxes for Street Lighting Network	26	20-Dec-26	18-Jan-27	16-Oct-25	15-Nov-25	0%	4,081	4,081
PRO-R17-SL-DL-	Material Delivery & Site Inspection of Cable Lugs for Street Lighting Network	26	19-Jan-27	17-Feb-27	16-Nov-25	15-Dec-25	0%	0	0
Road 16 Local 1 (527 LM)		78	20-Dec-26	24-Mar-27	16-Oct-25	14-Jan-26	0%	8,263	8,263
Lighting Poles Works		26	20-Dec-26	18-Jan-27	16-Oct-25	15-Nov-25	0%	4,112	4,112

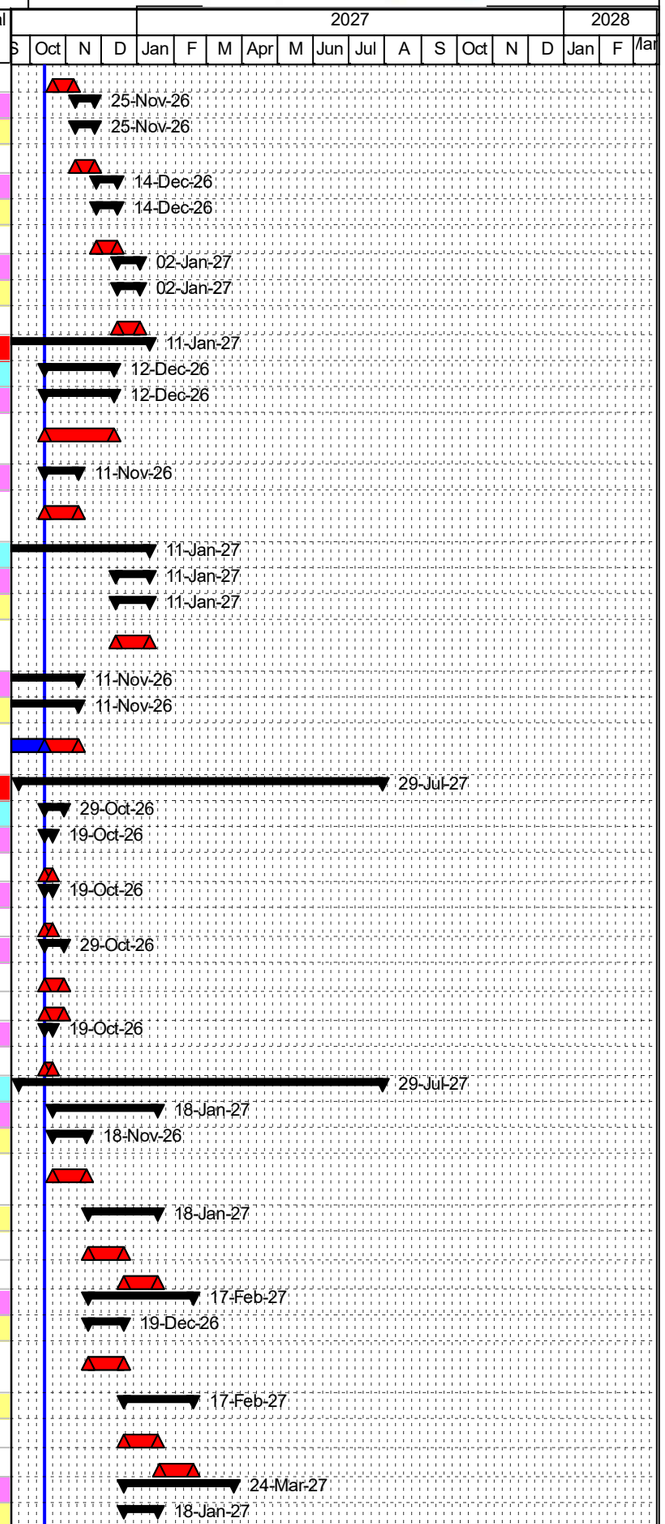

Primary Baseline | Actual Work | Summary
Remaining Work | Baseline Milestone
Critical Remaining Work | Milestone

Date	Revision	Checked	Approved
13-Oct-26	Third Industrial City		


Activity ID	Activity Name	Original Duration	Start	Finish	BL Project Start	BL Project Finish	Performance % Complete	Budgeted Total Cost	Remaining Total Cost
PRO-R16-SL-DL-14	Material Delivery & Site Inspection of Lighting Fixtures for Street Lighting Network	26	20-Dec-26	18-Jan-27	16-Oct-25	15-Nov-25	0%	4,112	4,112
Termination and Testing Works		52	19-Jan-27	24-Mar-27	16-Nov-25	14-Jan-26	0%	4,150	4,150
PRO-R16-SL-DL-	Material Delivery & Site Inspection of Fuse Boxes for Street Lighting Network	26	19-Jan-27	17-Feb-27	16-Nov-25	15-Dec-25	0%	4,150	4,150
PRO-R16-SL-DL-	Material Delivery & Site Inspection of Cable Lugs for Street Lighting Network	26	18-Feb-27	24-Mar-27	16-Dec-25	14-Jan-26	0%	0	0
Road 15 Local 1 (556 LM)		78	19-Jan-27	24-Apr-27	16-Nov-25	14-Feb-26	0%	9,493	9,493
Lighting Poles Works		26	19-Jan-27	17-Feb-27	16-Nov-25	15-Dec-25	0%	4,470	4,470
PRO-R15-SL-DL-14	Material Delivery & Site Inspection of Lighting Fixtures for Street Lighting Network	26	19-Jan-27	17-Feb-27	16-Nov-25	15-Dec-25	0%	4,470	4,470
Termination and Testing Works		52	18-Feb-27	24-Apr-27	16-Dec-25	14-Feb-26	0%	5,023	5,023
PRO-R15-SL-DL-	Material Delivery & Site Inspection of Fuse Boxes for Street Lighting Network	26	18-Feb-27	24-Mar-27	16-Dec-25	14-Jan-26	0%	5,023	5,023
PRO-R15-SL-DL-	Material Delivery & Site Inspection of Cable Lugs for Street Lighting Network	26	25-Mar-27	24-Apr-27	15-Jan-26	14-Feb-26	0%	0	0
Road 10 Local 2 (2352 LM)		502	21-Sep-26 A	24-Apr-27	02-Aug-25	16-Mar-26	68.93%	149,438	149,438
Lighting Poles Works		26	18-Feb-27	24-Mar-27	16-Dec-25	14-Jan-26	0%	17,165	17,165
PRO-R10-SL-DL-14	Material Delivery & Site Inspection of Lighting Fixtures for Street Lighting Network	26	18-Feb-27	24-Mar-27	16-Dec-25	14-Jan-26	0%	17,165	17,165
Distribution Panel Board		26	21-Sep-26 A	11-Nov-26	02-Aug-25	31-Aug-25	80%	103,537	103,537
PRO-R10-SL-DL-16	Material Delivery & Site Inspection of Distrubution Panel Boards for Street Lighting Network	26	21-Sep-26 A	11-Nov-26	02-Aug-25	31-Aug-25	80%	103,537	103,537
Termination and Testing Works		52	21-Sep-26 A	24-Apr-27	15-Jan-26	16-Mar-26	80%	25,218	25,218
PRO-R10-SL-DL-	Material Delivery & Site Inspection of Fuse Boxes for Street Lighting Network	26	21-Sep-26 A	24-Mar-27	15-Jan-26	14-Feb-26	80%	25,218	25,218
PRO-R10-SL-DL-	Material Delivery & Site Inspection of Cable Lugs for Street Lighting Network	26	21-Sep-26 A	24-Apr-27	15-Feb-26	16-Mar-26	80%	0	0
Earthing System Works		26	20-Oct-26	18-Nov-26	02-Aug-25	31-Aug-25	0%	3,518	3,518
PRO-R10-SL-DL-15	Material Delivery & Site Inspection of Lighting Earthing for Street Lighting Network	26	20-Oct-26	18-Nov-26	02-Aug-25	31-Aug-25	0%	3,518	3,518
Road 14 Local 1 (584 LM)		52	25-Mar-27	30-May-27	15-Jan-26	19-Apr-26	0%	17,818	17,818
Lighting Poles Works		26	25-Mar-27	24-Apr-27	15-Jan-26	14-Feb-26	0%	9,812	9,812
PRO-R14-SL-DL-14	Material Delivery & Site Inspection of Lighting Fixtures for Street Lighting Network	26	25-Mar-27	24-Apr-27	15-Jan-26	14-Feb-26	0%	9,812	9,812
Termination and Testing Works		52	25-Mar-27	30-May-27	15-Feb-26	19-Apr-26	0%	8,006	8,006
PRO-R14-SL-DL-	Material Delivery & Site Inspection of Fuse Boxes for Street Lighting Network	26	25-Mar-27	24-Apr-27	15-Feb-26	16-Mar-26	0%	8,006	8,006
PRO-R14-SL-DL-	Material Delivery & Site Inspection of Cable Lugs for Street Lighting Network	26	25-Apr-27	30-May-27	17-Mar-26	19-Apr-26	0%	0	0
Road 09 Local 2 (2278 LM)		208	20-Oct-26	29-Jun-27	02-Aug-25	19-May-26	0%	46,239	46,239
Lighting Poles Works		26	25-Apr-27	30-May-27	15-Feb-26	16-Mar-26	0%	17,522	17,522
PRO-R09-SL-DL-14	Material Delivery & Site Inspection of Lighting Fixtures for Street Lighting Network	26	25-Apr-27	30-May-27	15-Feb-26	16-Mar-26	0%	17,522	17,522
Termination and Testing Works		52	25-Apr-27	29-Jun-27	17-Mar-26	19-May-26	0%	25,199	25,199
PRO-R09-SL-DL-	Material Delivery & Site Inspection of Fuse Boxes for Street Lighting Network	26	25-Apr-27	30-May-27	17-Mar-26	19-Apr-26	0%	25,199	25,199
PRO-R09-SL-DL-	Material Delivery & Site Inspection of Cable Lugs for Street Lighting Network	26	31-May-27	29-Jun-27	20-Apr-26	19-May-26	0%	0	0
Earthing System Works		26	20-Oct-26	18-Nov-26	02-Aug-25	31-Aug-25	0%	3,518	3,518
PRO-R09-SL-DL-15	Material Delivery & Site Inspection of Lighting Earthing for Street Lighting Network	26	20-Oct-26	18-Nov-26	02-Aug-25	31-Aug-25	0%	3,518	3,518
Road 11 Local 1 (670 LM)		52	31-May-27	29-Jul-27	17-Mar-26	23-Jun-26	0%	10,383	10,383
Lighting Poles Works		26	31-May-27	29-Jun-27	17-Mar-26	19-Apr-26	0%	5,006	5,006
PRO-R11-SL-DL-14	Material Delivery & Site Inspection of Lighting Fixtures for Street Lighting Network	26	31-May-27	29-Jun-27	17-Mar-26	19-Apr-26	0%	5,006	5,006
Termination and Testing Works		52	31-May-27	29-Jul-27	20-Apr-26	23-Jun-26	0%	5,376	5,376
PRO-R11-SL-DL-1	Material Delivery & Site Inspection of Fuse Boxes for Street Lighting Network	26	31-May-27	29-Jun-27	20-Apr-26	19-May-26	0%	5,376	5,376
PRO-R11-SL-DL-1	Material Delivery & Site Inspection of Cable Lugs for Street Lighting Network	26	30-Jun-27	29-Jul-27	20-May-26	23-Jun-26	0%	0	0
Superstructure Works		414	29-Oct-25 A	20-Jan-27	13-Aug-25	14-Feb-26	95.27%	593,674	593,674
Manufacturing of Material		60	13-Oct-26	21-Dec-26	16-Aug-25	25-Oct-25	0%	0	0
Storm Drainage Ponds (PO-J1 , PO-J2)		60	13-Oct-26	21-Dec-26	16-Aug-25	25-Oct-25	0%	0	0
PRO-DPO-CV-MF-2(	Manufacturing of Civil Works for Storm Drainage Ponds (PO-J2)	60	13-Oct-26	21-Dec-26	16-Aug-25	25-Oct-25	0%	0	0
1st Material Delivery & Site Inspection		86	13-Oct-26	20-Jan-27	13-Aug-25	24-Nov-25	0%	0	0
Sewage Pump Stations (PS 06)		40	13-Oct-26	28-Nov-26	13-Aug-25	29-Sep-25	0%	0	0

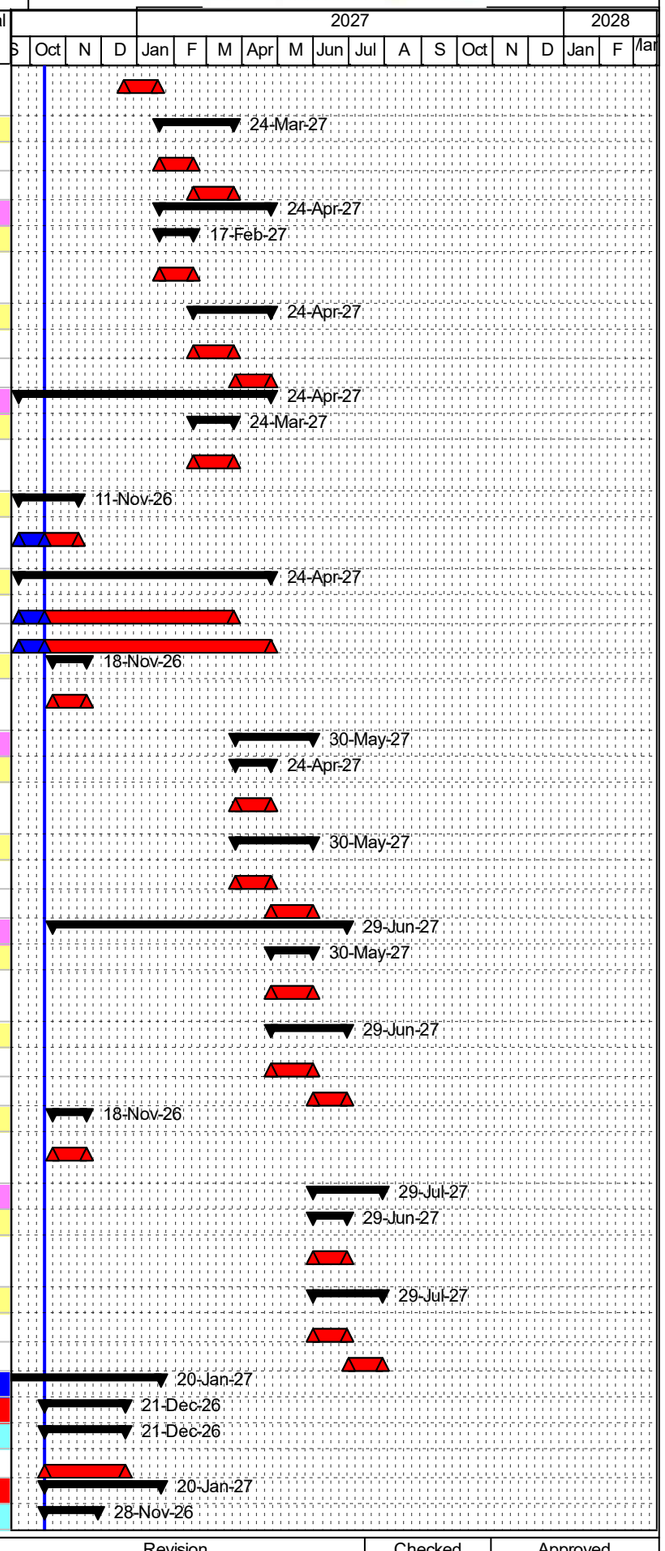

Primary Baseline
Actual Work
Summary
Remaining Work
Baseline Milestone
Critical Remaining Work
Milestone

Date	Revision	Checked	Approved
13-Oct-26	Third Industrial City		


Activity ID	Activity Name	Original Duration	Start	Finish	BL Project Start	BL Project Finish	Performance % Complete	Budgeted Total Cost	Remaining Total Cost
PRO-SPS-CV-1DL-1	1ST Material Delivery for Civil Works for Sewage Pump Stations (PS 06)	40	13-Oct-26	28-Nov-26	13-Aug-25	29-Sep-25	0%	0	0
Storm Drainage Ponds (PO-J1 , PO-J2)		26	22-Dec-26	20-Jan-27	26-Oct-25	24-Nov-25	0%	0	0
PRO-DPO-CV-1DL-2	1ST Material Delivery for Civil Works for Storm Drainage Ponds (PO-J2)	26	22-Dec-26	20-Jan-27	26-Oct-25	24-Nov-25	0%	0	0
Material Delivery & Site Inspection		130	29-Oct-25 A	20-Jan-27	15-Sep-25	14-Feb-26	95.27%	593,674	593,674
Storm Drainage Ponds (PO-J1 , PO-J2)		130	29-Oct-25 A	20-Jan-27	15-Sep-25	14-Feb-26	95.27%	593,674	593,674
PRO-DPO-CV-DL-10	Material Delivery & Site Inspection for Civil Works for Storm Drainage Ponds (PO-J1)	70	29-Oct-25 A	02-Jan-27	15-Sep-25	06-Dec-25	97%	508,118	508,118
PRO-DPO-CV-DL-20	Material Delivery & Site Inspection for Civil Works for Storm Drainage Ponds (PO-J2)	70	09-Sep-26 A	20-Jan-27	25-Nov-25	14-Feb-26	85%	85,556	85,556
Long Lead Time Items		50	05-Oct-26 A	09-Dec-26	05-Jul-26	31-Aug-26	40%	1,035,904	1,035,904
Superstructure Works		50	05-Oct-26 A	09-Dec-26	05-Jul-26	31-Aug-26	40%	1,035,904	1,035,904
Sewage Pump Stations (PS 06)		50	05-Oct-26 A	09-Dec-26	05-Jul-26	31-Aug-26	40%	1,035,904	1,035,904
Material Site Inspection		50	05-Oct-26 A	09-Dec-26	05-Jul-26	31-Aug-26	40%	1,035,904	1,035,904
PRO-SPS7-LL-MSI-10	Material Site Inspection for Electromechanical Works for Sewage Pump Stations (PS06)	50	05-Oct-26 A	09-Dec-26	05-Jul-26	31-Aug-26	40%	1,035,904	1,035,904
Construction Works		726	10-Nov-25 A	06-Dec-27	19-Mar-25	28-Dec-26	22.56%	29,449,451	28,717,979
Infrastructure Networks		726	10-Nov-25 A	06-Dec-27	19-Mar-25	28-Dec-26	26.84%	24,753,896	24,022,424
Phase 2 Block "J"		639	10-Nov-25 A	15-Sep-27	19-Mar-25	19-Nov-26	33.76%	15,357,323	14,727,808
Rising Main Network		367	17-Jan-26 A	05-Nov-26	27-Sep-25	13-Nov-25	82.1%	2,786,828	2,397,374
Main Line Sections		42	25-Feb-26 A	05-Nov-26	27-Sep-25	13-Nov-25	95.75%	1,336,086	1,336,086
CO-RM-SW-300	Pipes Laying Works for Main Lines of Rising Main Network	21	25-Feb-26 A	05-Nov-26	27-Sep-25	20-Oct-25	98%	1,169,075	1,169,075
CO-RM-SW-310	Trench Backfilling and Compaction Works for Main Lines of Rising Main Network	21	01-Sep-26 A	05-Nov-26	21-Oct-25	13-Nov-25	80%	167,011	167,011
Manholes		366	17-Jan-26 A	19-Oct-26	28-Sep-25	18-Oct-25	88.16%	835,054	835,054
CO-RM-SW-330	Installation RC Footing Works for Main Line Manholes of Rising Main Network	3	17-Jan-26 A	15-Oct-26	28-Sep-25	30-Sep-25	97%	66,804	66,804
CO-RM-SW-340	Install Grp Liner Wall Works for Main Line Manholes of Rising Main Network	6	17-Jan-26 A	19-Oct-26	01-Oct-25	07-Oct-25	98%	501,032	501,032
CO-RM-SW-350	Pouring Grp Liner Wall Works for Main Line Manholes of Rising Main Network	3	18-Sep-26 A	15-Oct-26	08-Oct-25	11-Oct-25	90%	66,804	66,804
CO-RM-SW-360	Backfilling Works for Main Line Manholes of Rising Main Network	5	21-Sep-26 A	18-Oct-26	12-Oct-25	16-Oct-25	80%	100,206	100,206
CO-RM-SW-370	Testing Works for Main Line Manholes of Rising Main Network	1	01-Oct-26 A	13-Oct-26	18-Oct-25	18-Oct-25	40%	100,206	100,206
Valves Chamber		329	14-May-26 A	01-Nov-26	05-Oct-25	01-Nov-25	44.28%	615,689	226,234
CO-RM-SW-400	RC Wall Works for Valve Chambers and Washout chamber of Rising Main Network	7	14-May-26 A	13-Oct-26	05-Oct-25	12-Oct-25	70%	389,454	0
CO-RM-SW-410	RC Slab Works for Valve Chambers and Washout chamber of Rising Main Network	7	13-Oct-26	20-Oct-26	13-Oct-25	20-Oct-25	0%	43,273	43,273
CO-RM-SW-420	Insulation Works for Valve Chambers and Washout chamber of Rising Main Network	2	21-Oct-26	22-Oct-26	21-Oct-25	22-Oct-25	0%	43,273	43,273
CO-RM-SW-430	Backfilling Works for Valve Chambers and Washout chamber of Rising Main Network	5	24-Oct-26	28-Oct-26	23-Oct-25	28-Oct-25	0%	53,143	53,143
CO-RM-SW-440	Testing and Covering Works for Valve Chambers and Washout chamber of Rising Main Network	3	29-Oct-26	01-Nov-26	29-Oct-25	01-Nov-25	0%	86,545	86,545
Road 09 Local 2 (2278 LM)		639	10-Nov-25 A	11-Sep-27	21-Jul-25	01-Oct-26	30.44%	6,065,924	5,931,578
SW_1		557	02-May-26 A	11-Sep-27	11-Aug-25	24-Sep-26	32.32%	3,211,612	3,211,612
Sewage Network		1	13-Oct-26	13-Oct-26	11-Aug-25	11-Aug-25	0%	35,494	35,494
Manholes		1	13-Oct-26	13-Oct-26	11-Aug-25	11-Aug-25	0%	35,494	35,494
CO-R09.S01-SW-1	Testing Works for Main Line Manholes of Sewage Network-[Road 09] -[SW-1]	1	13-Oct-26	13-Oct-26	11-Aug-25	11-Aug-25	0%	35,494	35,494
Storm Drainage Network		317	27-Jun-26 A	28-Oct-26	05-Oct-25	18-Nov-25	74.67%	287,863	287,863
Manholes		2	07-Oct-26 A	14-Oct-26	05-Oct-25	06-Oct-25	40%	38,389	38,389
CO-R09.S01-SD-2	Testing Works for Manholes of Storm Drainage Network-[Road 09] -[SW-1]	2	07-Oct-26 A	14-Oct-26	05-Oct-25	06-Oct-25	40%	38,389	38,389
Catch Basin Sections		317	27-Jun-26 A	28-Oct-26	15-Oct-25	18-Nov-25	80%	249,475	249,475
CO-R09.S01-SD-14	Trench Excavation and Bedding Works for Catch Basins of Storm Drainage Network-[Road 09] -[SW-1]	6	27-Jun-26 A	19-Oct-26	15-Oct-25	21-Oct-25	90%	41,579	41,579
CO-R09.S01-SD-15	Installation and Pipes Laying Connection Works for Catch Basins of Storm Drainage Network-[Road 09] -[SW-1]	7	29-Jun-26 A	20-Oct-26	22-Oct-25	29-Oct-25	90%	124,737	124,737

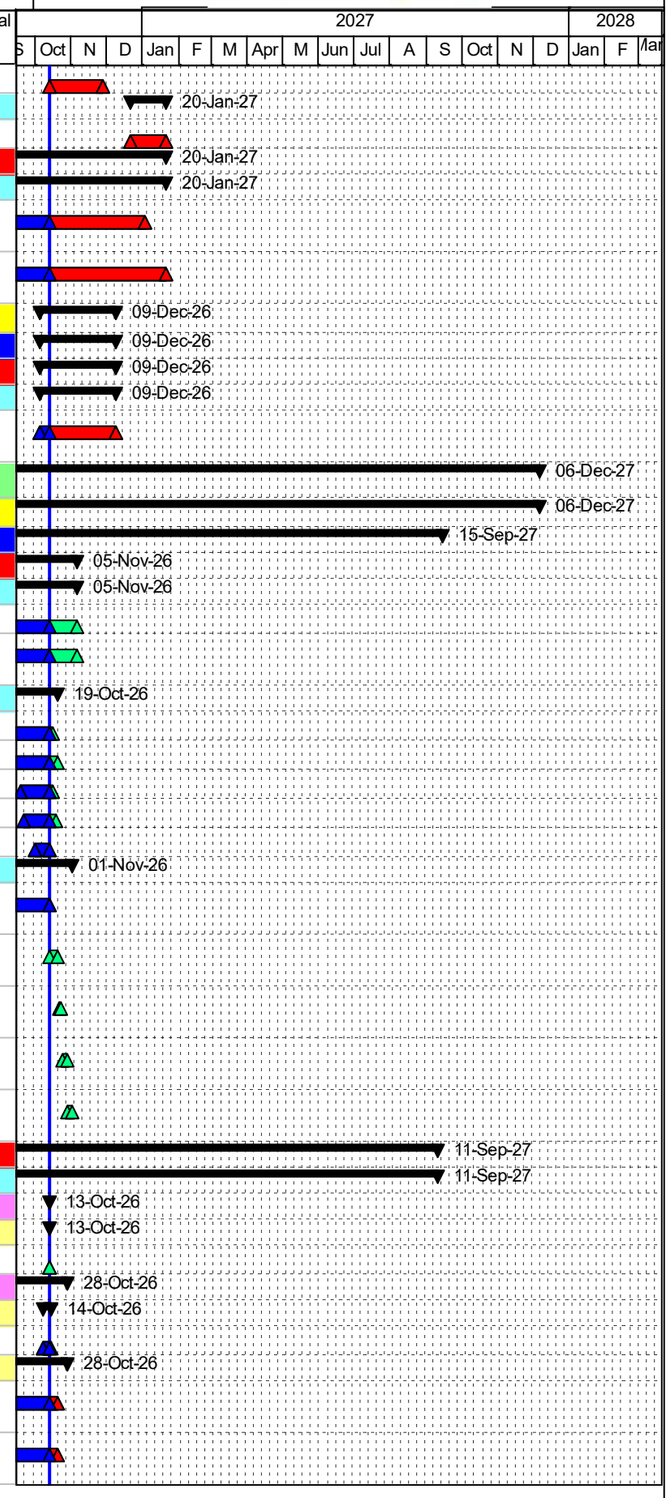

Primary Baseline | Actual Work | Summary
Remaining Work | Baseline Milestone
Critical Remaining Work | Milestone

Date	Revision	Checked	Approved
13-Oct-26	Third Industrial City		


Activity ID	Activity Name	Original Duration	Start	Finish	BL Project Start	BL Project Finish	Performance % Complete	Budgeted Total Cost	Remaining Total Cost
CO-R09.S01-SD-17	Trench Backfilling and Compaction Works for Catch Basins of Storm Drainage Network-[Road 09] -[SW-1]	10	03-Aug-26 A	28-Oct-26	08-Nov-25	18-Nov-25	90%	55,439	55,439
CO-R09.S01-SD-16	Testing Works for Catch Basins of Storm Drainage Network-[Road 09] -[SW-1]	7	21-Oct-26	28-Oct-26	30-Oct-25	06-Nov-25	0%	27,719	27,719
Irrigation Network		273	02-May-26 A	01-Nov-26	09-Dec-25	28-Dec-25	33.92%	140,091	140,091
Main Line Pipes		273	02-May-26 A	01-Nov-26	09-Dec-25	28-Dec-25	33.92%	140,091	140,091
CO-R09.S01-IR-120	Installation Works for Main Line Valves of Irrigation Network-[Road 09] -[SW-1]	7	02-May-26 A	20-Oct-26	09-Dec-25	16-Dec-25	40%	118,784	118,784
CO-R09.S01-IR-140	Trench Backfilling and Compaction Works for Main Lines of Irrigation Network-[Road 09] -[SW-1]	10	21-Oct-26	01-Nov-26	17-Dec-25	28-Dec-25	0%	21,307	21,307
Street Lighting Network		237	02-Nov-26	15-Aug-27	29-Dec-25	13-Aug-26	0%	273,720	273,720
Lighting Poles Works		68	02-Nov-26	19-Jan-27	29-Dec-25	30-Apr-26	0%	140,447	140,447
CO-R09.S01-SL-100	Foundation Excavation Works for Lighting Poles of Street Lighting Network-[Road 09] -[SW-1]	10	02-Nov-26	12-Nov-26	29-Dec-25	08-Jan-26	0%	4,664	4,664
CO-R09.S01-SL-110	Installation Works for Lighting Poles Foundation of Street Lighting Network-[Road 09] -[SW-1]	12	14-Nov-26	26-Nov-26	10-Jan-26	22-Jan-26	0%	17,827	17,827
CO-R09.S01-SL-120	Installation Works for Lighting Poles of Street Lighting Network-[Road 09] -[SW-1]	11	19-Dec-26	30-Dec-26	14-Feb-26	25-Feb-26	0%	51,299	51,299
CO-R09.S01-SL-210	Backfilling Works for Lighting Poles of Street Lighting Network-[Road 09] -[SW-1]	12	31-Dec-26	13-Jan-27	12-Apr-26	25-Apr-26	0%	18,654	18,654
CO-R09.S01-SL-130	Installation Works for Lighting Fixtures With Drop Wire of Street Lighting Network-[Road 09] -[SW-1]	12	06-Jan-27	19-Jan-27	18-Apr-26	30-Apr-26	0%	29,350	29,350
CO-R09.S01-SL-2	Testing Works for Lighting Poles of Street Lighting Network-[Road 09] -[SW-1]	5	14-Jan-27	19-Jan-27	26-Apr-26	30-Apr-26	0%	18,654	18,654
Cabling Works		30	14-Nov-26	17-Dec-26	10-Jan-26	12-Feb-26	0%	94,452	94,452
CO-R09.S01-SL-140	Trench Excavation and Bedding Works for Street Lighting Network-[Road 09] -[SW-1]	10	14-Nov-26	24-Nov-26	10-Jan-26	20-Jan-26	0%	0	0
CO-R09.S01-SL-1	Cable Laying Works for Street Lighting Network-[Road 09] -[SW-1]	10	25-Nov-26	06-Dec-26	21-Jan-26	01-Feb-26	0%	87,705	87,705
CO-R09.S01-SL-160	Trench Backfilling and Compaction Works for Street Lighting Network-[Road 09] -[SW-1]	10	07-Dec-26	17-Dec-26	02-Feb-26	12-Feb-26	0%	6,747	6,747
Distrubution Panel Boards		39	01-Jul-27	15-Aug-27	30-Jun-26	13-Aug-26	0%	38,822	38,822
CO-R09.S01-SL-170	Foundation Excavation Works For Panel Boards of Street Lighting Network-[Road 09] -[SW-1]	15	01-Jul-27	18-Jul-27	30-Jun-26	16-Jul-26	0%	0	0
CO-R09.S01-SL-180	Installation Works for Panel Board Concrete Foundations of Street Lighting Network-[Road 09] -[SW-1]	12	19-Jul-27	01-Aug-27	18-Jul-26	30-Jul-26	0%	0	0
CO-R09.S01-SL-190	Installation Works for Lighting Panel Boards of Street Lighting Network-[Road 09] -[SW-1]	12	02-Aug-27	15-Aug-27	01-Aug-26	13-Aug-26	0%	0	0
CO-R09.S01-SL-220	A wall of concrete blocks to install the KWH meter of Street Lighting Network-[Road 09] -[SW-1]	12	02-Aug-27	15-Aug-27	01-Aug-26	13-Aug-26	0%	38,822	38,822
Medium Voltage Network		322	30-Sep-26 A	27-Dec-26	14-Feb-26	03-Mar-26	29.38%	1,203,791	1,203,791
Cabling Works		322	30-Sep-26 A	27-Dec-26	14-Feb-26	03-Mar-26	29.38%	1,203,791	1,203,791
CO-R09.S01-MV-10	Trench Excavation and Bedding Works for Medium Voltage Network-[Road 09] -[SW-1]	4	30-Sep-26 A	17-Dec-26	14-Feb-26	17-Feb-26	40%	138,631	138,631
CO-R09.S01-MV-1	Cable Laying Works for Medium Voltage Network-[Road 09] -[SW-1]	5	07-Oct-26 A	19-Dec-26	18-Feb-26	23-Feb-26	40%	745,612	745,612
CO-R09.S01-MV-12	Trench Backfilling and Compaction Works for Medium Voltage Network-[Road 09] -[SW-1]	7	20-Dec-26	27-Dec-26	24-Feb-26	03-Mar-26	0%	319,548	319,548
Telecom Network		38	28-Dec-26	09-Feb-27	03-May-26	20-Jun-26	0%	166,585	166,585
Ducts Works		12	28-Dec-26	10-Jan-27	03-May-26	16-May-26	0%	132,124	132,124
CO-R09.S01-TE-100	Trench Excavation and Bedding Works for Ducts of Telecom Network-[Road 09] -[SW-1]	2	28-Dec-26	29-Dec-26	03-May-26	04-May-26	0%	13,266	13,266
CO-R09.S01-TE-1	Pipes Laying Works for Ducts of Telecom Network-[Road 09] -[SW-1]	4	30-Dec-26	03-Jan-27	05-May-26	09-May-26	0%	79,228	79,228
CO-R09.S01-TE-1	Pouring Plain Concrete Above Ducts of Telecom Network-[Road 09] -[SW-1]	2	04-Jan-27	05-Jan-27	10-May-26	11-May-26	0%	13,266	13,266
CO-R09.S01-TE-130	Trench Backfilling and Compaction Works for Ducts of Telecom Network-[Road 09] -[SW-1]	4	06-Jan-27	10-Jan-27	12-May-26	16-May-26	0%	26,365	26,365
Manholes Works		36	30-Dec-26	09-Feb-27	05-May-26	20-Jun-26	0%	34,461	34,461
CO-R09.S01-TE-1	Excavation Works for Manholes of Telecom Network-[Road 09] -[SW-1]	12	30-Dec-26	12-Jan-27	05-May-26	18-May-26	0%	7,515	7,515

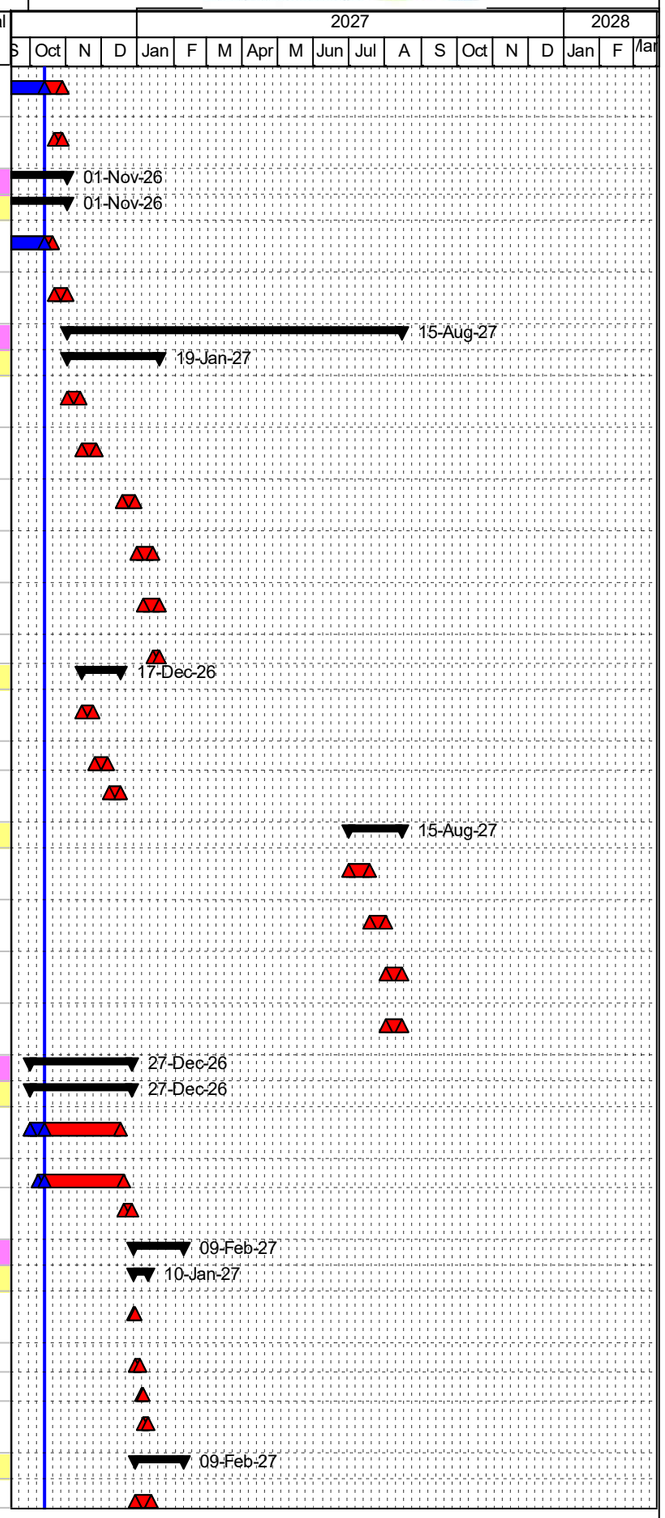

Primary Baseline
Remaining Work
Critical Remaining Work
Actual Work
Baseline Milestone
Milestone
Summary

Date	Revision	Checked	Approved
13-Oct-26	Third Industrial City		


Activity ID	Activity Name	Original Duration	Start	Finish	BL Project Start	BL Project Finish	Performance % Complete	Budgeted Total Cost	Remaining Total Cost
CO-R09.S01-TE-1	Installation Works for Manholes of Telecom Network-[Road 09] -[SW-1]	12	13-Jan-27	26-Jan-27	19-May-26	06-Jun-26	0%	19,430	19,430
CO-R09.S01-TE-1	Backfilling Works for Manholes of Telecom Network-[Road 09] -[SW-1]	12	27-Jan-27	09-Feb-27	07-Jun-26	20-Jun-26	0%	7,515	7,515
Road Works		203	10-Jun-26 A	11-Sep-27	21-Jun-26	24-Sep-26	38.2%	1,104,067	1,104,067
Pre-Bituminous Construction		203	10-Jun-26 A	13-Feb-27	21-Jun-26	18-Jul-26	35.37%	890,287	890,287
CO-R09.S01-RD-I	Capping and Subgrade Layer for Road Works-[Road 09] -[SW-1]	21	10-Jun-26 A	09-Feb-27	21-Jun-26	14-Jul-26	60%	524,764	524,764
CO-R09.S01-RD-I	Aggregate Base Course Layer for Road Works-[Road 09] -[SW-1]	21	20-Jan-27	13-Feb-27	24-Jun-26	18-Jul-26	0%	365,524	365,524
Pavement Works		12	25-Aug-26 A	11-Sep-27	09-Sep-26	24-Sep-26	50%	213,780	213,780
CO-R09.S01-RD-I	Fixing of Interlock Tiles for Sidewalks Pavement-[Road 09] -[SW-1]	12	25-Aug-26 A	11-Sep-27	09-Sep-26	24-Sep-26	50%	213,780	213,780
SW_2		639	10-Nov-25 A	11-Sep-27	21-Jul-25	01-Oct-26	28.33%	2,854,312	2,719,966
Sewage Network		377	10-Nov-25 A	26-Oct-26	21-Jul-25	31-Aug-25	92.79%	289,559	155,213
Main Line Sections		36	10-Nov-25 A	26-Oct-26	21-Jul-25	31-Aug-25	94.44%	284,502	150,155
CO-R09.S02-SW-10	Trench Excavation and Bedding Works for Main Lines of Sewage Network-[Road 09]-[SW-2]	12	10-Nov-25 A	26-Oct-26	21-Jul-25	03-Aug-25	95%	63,215	21,072
CO-R09.S02-SW-	Pipes Laying Works for Main Lines of Sewage Network-[Road 09]-[SW-2]	12	15-Feb-26 A	26-Oct-26	04-Aug-25	17-Aug-25	95%	189,644	110,626
CO-R09.S02-SW-13	Trench Backfilling and Compaction Works for Main Lines of Sewage Network-[Road 09]-[SW-2]	12	02-May-26 A	26-Oct-26	18-Aug-25	31-Aug-25	90%	31,643	18,458
Manholes		1	13-Oct-26	13-Oct-26	25-Aug-25	25-Aug-25	0%	5,057	5,057
CO-R09.S02-SW-	Testing Works for Main Line Manholes of Sewage Network-[Road 09]-[SW-2]	1	13-Oct-26	13-Oct-26	25-Aug-25	25-Aug-25	0%	5,057	5,057
Storm Drainage Network		298	24-Jun-26 A	25-Oct-26	23-Oct-25	20-Dec-25	69.33%	287,863	287,863
Manholes		2	13-Oct-26	14-Oct-26	23-Oct-25	25-Oct-25	0%	38,389	38,389
CO-R09.S02-SD-	Testing Works for Manholes of Storm Drainage Network-[Road 09]-[SW-2]	2	13-Oct-26	14-Oct-26	23-Oct-25	25-Oct-25	0%	38,389	38,389
Catch Basin Sections		298	24-Jun-26 A	25-Oct-26	03-Nov-25	20-Dec-25	80%	249,475	249,475
CO-R09.S02-SD-14	Trench Excavation and Bedding Works for Catch Basins of Storm Drainage Network-[Road 09]-[SW-2]	6	24-Jun-26 A	19-Oct-26	03-Nov-25	09-Nov-25	90%	41,579	41,579
CO-R09.S02-SD-15	Installation and Pipes Laying Connection Works for Catch Basins of Storm Drainage Network-[Road 09]-[SW-2]	7	25-Jun-26 A	20-Oct-26	30-Nov-25	07-Dec-25	90%	124,737	124,737
CO-R09.S02-SD-17	Trench Backfilling and Compaction Works for Catch Basins of Storm Drainage Network-[Road 09]-[SW-2]	7	28-Jun-26 A	25-Oct-26	13-Dec-25	20-Dec-25	90%	55,439	55,439
CO-R09.S02-SD-	Testing Works for Catch Basins of Storm Drainage Network-[Road 09]-[SW-2]	4	21-Oct-26	25-Oct-26	08-Dec-25	11-Dec-25	0%	27,719	27,719
Potable Water Network		310	27-Jun-26 A	21-Mar-27	03-Nov-25	29-Dec-25	53.96%	432,458	432,458
Main Line Sections		49	27-Jun-26 A	21-Mar-27	03-Nov-25	29-Dec-25	91.54%	254,908	254,908
CO-R09.S02-PW-10	Trench Excavation and Bedding Works for Main Lines of Potable Water Network-[Road 09]-[SW-2]	7	27-Jun-26 A	20-Oct-26	03-Nov-25	10-Nov-25	95%	78,464	78,464
CO-R09.S02-PW-11	Pipes Laying and accessories for Main Lines of Potable Water Network-[Road 09]-[SW-2]	8	30-Jun-26 A	21-Mar-27	10-Dec-25	18-Dec-25	90%	96,161	96,161
CO-R09.S02-PW-13	Trench Backfilling and Compaction Works for Main Lines of Potable Water Network-[Road 09]-[SW-2]	8	01-Jul-26 A	21-Mar-27	21-Dec-25	29-Dec-25	90%	80,283	80,283
Valve Chamber		6	21-Oct-26	27-Oct-26	11-Nov-25	17-Nov-25	0%	63,935	63,935
CO-R09.S02-PW-21	Installation Works for Main Line Valves and Valve Chambers of Potable Water Network-[Road 09]-[SW-2]	6	21-Oct-26	27-Oct-26	11-Nov-25	17-Nov-25	0%	63,935	63,935
Fire Hydrant		16	21-Oct-26	08-Nov-26	11-Nov-25	29-Dec-25	0%	113,615	113,615
CO-R09.S02-PW-14	Excavation Works for Fire Hydrants of Potable Water Network-[Road 09]-[SW-2]	5	21-Oct-26	26-Oct-26	11-Nov-25	16-Nov-25	0%	17,042	17,042
CO-R09.S02-PW-15	Installation Works for Fire Hydrant of Potable Water Network-[Road 09]-[SW-2]	6	27-Oct-26	02-Nov-26	17-Dec-25	23-Dec-25	0%	73,850	73,850
CO-R09.S02-PW-16	Trench Backfilling and Compaction Works for Fire Hydrants of Potable Water Network-[Road 09]-[SW-2]	5	03-Nov-26	08-Nov-26	24-Dec-25	29-Dec-25	0%	22,723	22,723
Street Lighting Network		130	22-Mar-27	26-Aug-27	30-Dec-25	25-Aug-26	0%	573,623	573,623
Lighting Poles Works		58	22-Mar-27	02-Jun-27	30-Dec-25	01-Jun-26	0%	140,447	140,447
CO-R09.S02-SL-10	Foundation Excavation Works for Lighting Poles of Street Lighting Network-[Road 09]-[SW-2]	9	22-Mar-27	31-Mar-27	30-Dec-25	08-Jan-26	0%	4,664	4,664
CO-R09.S02-SL-11	Installation Works for Lighting Poles Foundation of Street Lighting Network-[Road 09]-[SW-2]	9	01-Apr-27	11-Apr-27	10-Jan-26	19-Jan-26	0%	17,827	17,827
CO-R09.S02-SL-12	Installation Works for Lighting Poles of Street Lighting Network-[Road 09]-[SW-2]	9	12-Apr-27	21-Apr-27	08-Feb-26	17-Feb-26	0%	51,299	51,299

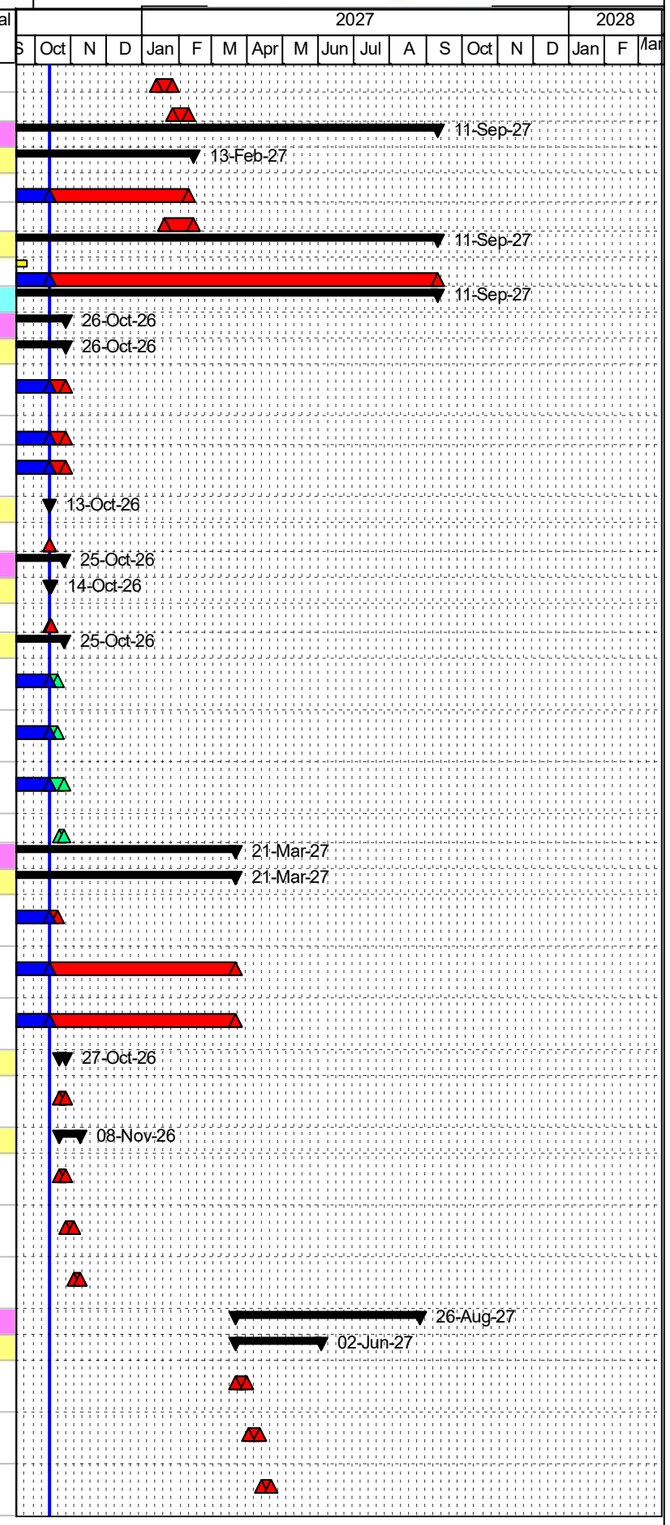

Primary Baseline
Actual Work
Summary
Remaining Work
Baseline Milestone
Critical Remaining Work
Milestone

Date	Revision	Checked	Approved
13-Oct-26	Third Industrial City		


Activity ID	Activity Name	Original Duration	Start	Finish	BL Project Start	BL Project Finish	Performance % Complete	Budgeted Total Cost	Remaining Total Cost
CO-R09.S02-SL-21(	Backfilling Works for Lighting Poles of Street Lighting Network-[Road 09]-[SW-2]	20	22-Apr-27	20-May-27	26-Apr-26	18-May-26	0%	18,654	18,654
CO-R09.S02-SL-13(	Installation Works for Lighting Fixtures With Drop Wire of Street Lighting Network-[Road 09]-[SW-2]	17	09-May-27	02-Jun-27	09-May-26	01-Jun-26	0%	29,350	29,350
CO-R09.S02-SL-2	Testing Works for Lighting Poles of Street Lighting Network-[Road 09]-[SW-2]	8	22-May-27	30-May-27	19-May-26	01-Jun-26	0%	18,654	18,654
Cabling Works		30	22-Apr-27	01-Jun-27	18-Feb-26	28-Mar-26	0%	94,452	94,452
CO-R09.S02-SL-14(	Trench Excavation and Bedding Works for Street Lighting Network-[Road 09]-[SW-2]	10	22-Apr-27	03-May-27	18-Feb-26	01-Mar-26	0%	0	0
CO-R09.S02-SL-1	Cable Laying Works for Street Lighting Network-[Road 09]-[SW-2]	10	04-May-27	20-May-27	02-Mar-26	12-Mar-26	0%	87,705	87,705
CO-R09.S02-SL-16(	Trench Backfilling and Compaction Works for Street Lighting Network-[Road 09]-[SW-2]	10	22-May-27	01-Jun-27	14-Mar-26	28-Mar-26	0%	6,747	6,747
Distrubution Panel Boards		48	01-Jul-27	26-Aug-27	30-Jun-26	25-Aug-26	0%	338,724	338,724
CO-R09.S02-SL-17(	Foundation Excavation Works For Panel Boards of Street Lighting Network-[Road 09]-[SW-2]	10	01-Jul-27	12-Jul-27	30-Jun-26	11-Jul-26	0%	43,293	43,293
CO-R09.S02-SL-18(	Installation Works for Panel Board Concrete Foundations of Street Lighting Network-[Road 09]-[SW-2]	10	13-Jul-27	24-Jul-27	12-Jul-26	22-Jul-26	0%	48,506	48,506
CO-R09.S02-SL-19(	Installation Works for Lighting Panel Boards of Street Lighting Network-[Road 09]-[SW-2]	10	25-Jul-27	04-Aug-27	23-Jul-26	03-Aug-26	0%	177,856	177,856
CO-R09.S02-SL-22(	A wall of concrete blocks to install the KWH meter of Street Lighting Network-[Road 09]-[SW-2]	18	05-Aug-27	26-Aug-27	04-Aug-26	25-Aug-26	0%	69,068	69,068
Telecom Network		47	11-Jan-27	07-Mar-27	17-May-26	14-Jul-26	0%	166,742	166,742
Ducts Works		24	11-Jan-27	07-Feb-27	17-May-26	17-Jun-26	0%	132,124	132,124
CO-R09.S02-TE-10(	Trench Excavation and Bedding Works for Ducts of Telecom Network-[Road 09]-[SW-2]	3	11-Jan-27	13-Jan-27	17-May-26	19-May-26	0%	13,266	13,266
CO-R09.S02-TE-1	Pipes Laying Works for Ducts of Telecom Network-[Road 09]-[SW-2]	7	14-Jan-27	21-Jan-27	20-May-26	01-Jun-26	0%	79,228	79,228
CO-R09.S02-TE-1	Pouring Plain Concrete Above Ducts of Telecom Network-[Road 09]-[SW-2]	7	23-Jan-27	30-Jan-27	02-Jun-26	09-Jun-26	0%	13,266	13,266
CO-R09.S02-TE-13(	Trench Backfilling and Compaction Works for Ducts of Telecom Network-[Road 09]-[SW-2]	7	31-Jan-27	07-Feb-27	10-Jun-26	17-Jun-26	0%	26,365	26,365
Manholes Works		21	10-Feb-27	07-Mar-27	21-Jun-26	14-Jul-26	0%	34,618	34,618
CO-R09.S02-TE-1	Excavation Works for Manholes of Telecom Network-[Road 09]-[SW-2]	7	10-Feb-27	17-Feb-27	21-Jun-26	28-Jun-26	0%	6,300	6,300
CO-R09.S02-TE-1	Installation Works for Manholes of Telecom Network-[Road 09]-[SW-2]	7	18-Feb-27	27-Feb-27	29-Jun-26	06-Jul-26	0%	22,017	22,017
CO-R09.S02-TE-1	Backfilling Works for Manholes of Telecom Network-[Road 09]-[SW-2]	7	28-Feb-27	07-Mar-27	07-Jul-26	14-Jul-26	0%	6,300	6,300
Road Works		232	25-Aug-26 A	11-Sep-27	15-Jul-26	01-Oct-26	9.68%	1,104,067	1,104,067
Pre-Bituminous Construction		21	25-May-27	17-Jun-27	15-Jul-26	08-Aug-26	0%	890,287	890,287
CO-R09.S02-RD-I	Capping and Subgrade Layer for Road Works-[Road 09]-[SW-2]	12	25-May-27	07-Jun-27	15-Jul-26	28-Jul-26	0%	524,764	524,764
CO-R09.S02-RD-I	Aggregate Base Course Layer for Road Works-[Road 09]-[SW-2]	18	29-May-27	17-Jun-27	19-Jul-26	08-Aug-26	0%	365,524	365,524
Pavement Works		18	25-Aug-26 A	11-Sep-27	09-Sep-26	01-Oct-26	50%	213,780	213,780
CO-R09.S02-RD-I	Fixing of Interlock Tiles for Sidewalks Pavement-[Road 09]-[SW-2]	18	25-Aug-26 A	11-Sep-27	09-Sep-26	01-Oct-26	50%	213,780	213,780
Road 10 Local 2 (2352 LM)		417	17-Jun-26 A	11-Jul-27	23-Jul-25	01-Oct-26	13.81%	4,836,010	4,767,707
SW-3		193	25-Aug-26 A	11-Jul-27	15-Oct-25	29-Sep-26	5.06%	2,120,235	2,120,235
SW_3-East		193	25-Aug-26 A	11-Jul-27	15-Oct-25	29-Sep-26	4.57%	1,171,703	1,171,703
Potable Water Network		16	13-Oct-26	31-Oct-26	15-Oct-25	04-Nov-25	0%	138,829	138,829
Valve Chamber		16	13-Oct-26	31-Oct-26	15-Oct-25	02-Nov-25	0%	82,021	82,021
CO-R10.S03-ES-P'	Excavation Works for Main Line Valves and Valve Chambers of Potable Water Network-[Road 10]-[SW-3]	1	13-Oct-26	13-Oct-26	15-Oct-25	15-Oct-25	0%	1,161	1,161
CO-R10.S03-ES-P'	RC Footing Works for Main Line Valves and Valve Chambers of Potable Water Network-[Road 10]-[SW-3]	3	14-Oct-26	17-Oct-26	16-Oct-25	19-Oct-25	0%	6,529	6,529
CO-R10.S03-ES-P'	RC Wall Works for Main Line Valves and Valve Chambers of Potable Water Network-[Road 10]-[SW-3]	6	18-Oct-26	24-Oct-26	20-Oct-25	26-Oct-25	0%	15,234	15,234
CO-R10.S03-ES-P'	RC Slab Works for Main Line Valves and Valve Chambers of Potable Water Network-[Road 10]-[SW-3]	2	25-Oct-26	26-Oct-26	27-Oct-25	28-Oct-25	0%	8,705	8,705
CO-R10.S03-ES-P'	Insulation Works for Main Line Valves and Valve Chambers of Potable Water Network-[Road 10]-[SW-3]	1	27-Oct-26	27-Oct-26	29-Oct-25	29-Oct-25	0%	41,688	41,688
CO-R10.S03-ES-P'	Backfilling Works for Main Line Valves and Valve Chambers of Potable Water Network-[Road 10]-[SW-3]	3	28-Oct-26	31-Oct-26	30-Oct-25	02-Nov-25	0%	8,705	8,705

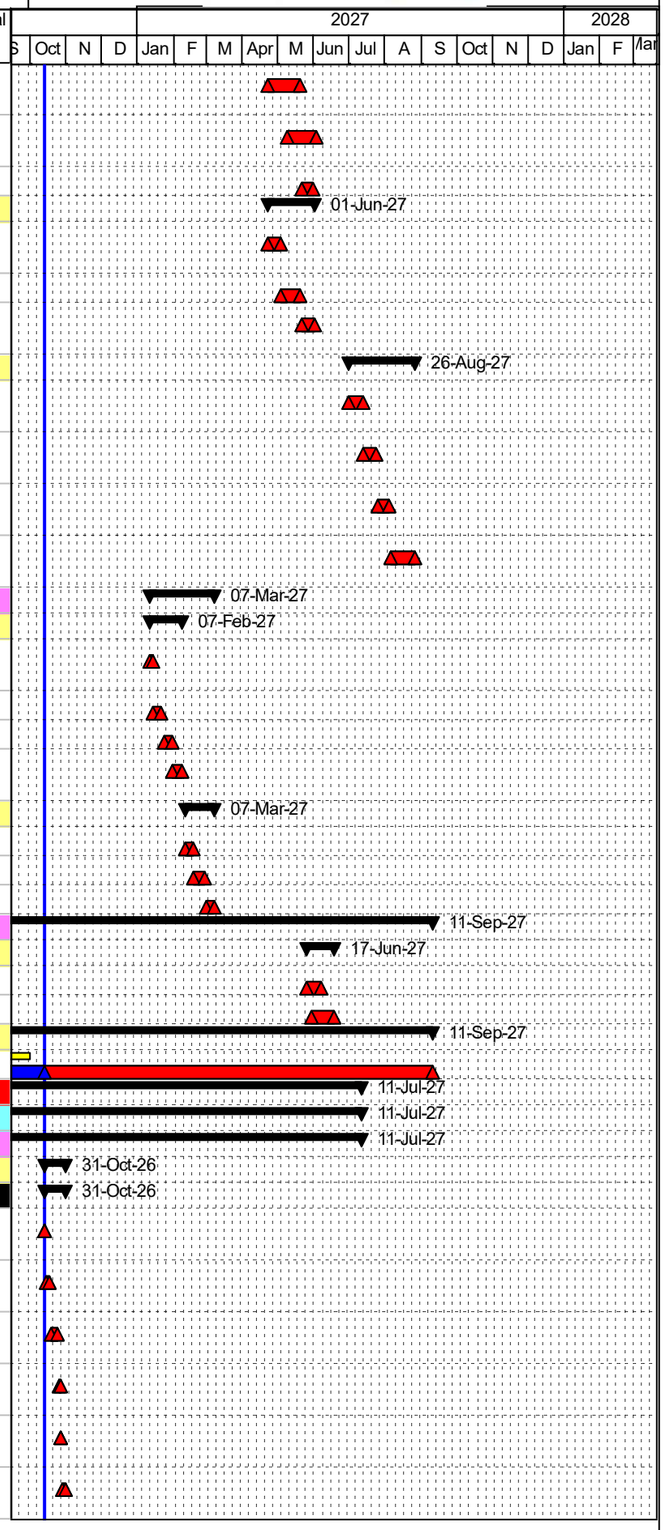

Primary Baseline
Remaining Work
Critical Remaining Work
Actual Work
Baseline Milestone
Milestone
Summary

Date	Revision	Checked	Approved
13-Oct-26	Third Industrial City		


Activity ID	Activity Name	Original Duration	Start	Finish	BL Project Start	BL Project Finish	Performance % Complete	Budgeted Total Cost	Remaining Total Cost
Fire Hydrant		15	13-Oct-26	29-Oct-26	19-Oct-25	04-Nov-25	0%	56,808	56,808
CO-R10.S03-ES-P	Excavation Works for Fire Hydrants of Potable Water Network-[Road 10]-[SW-3]	6	13-Oct-26	19-Oct-26	19-Oct-25	25-Oct-25	0%	8,521	8,521
CO-R10.S03-ES-P	Installation Works for Fire Hydrant of Potable Water Network-[Road 10]-[SW-3]	6	20-Oct-26	26-Oct-26	26-Oct-25	01-Nov-25	0%	36,925	36,925
CO-R10.S03-ES-P	Trench Backfilling and Compaction Works for Fire Hydrants of Potable Water Network-[Road 10]-[SW-3]	6	24-Oct-26	29-Oct-26	29-Oct-25	04-Nov-25	0%	11,362	11,362
Street Lighting Network		172	13-Oct-26	05-May-27	02-Dec-25	29-Jun-26	0%	398,748	398,748
Lighting Poles Works		33	13-Oct-26	19-Nov-26	02-Dec-25	16-Feb-26	0%	68,790	68,790
CO-R10.S03-ES-S	Foundation Excavation Works for Lighting Poles of Street Lighting Network-[Road 10]-[SW-3]	12	13-Oct-26	26-Oct-26	02-Dec-25	15-Dec-25	0%	2,284	2,284
CO-R10.S03-ES-S	Installation Works for Lighting Poles Foundation of Street Lighting Network-[Road 10]-[SW-3]	12	19-Oct-26	01-Nov-26	08-Dec-25	21-Dec-25	0%	8,731	8,731
CO-R10.S03-ES-S	Installation Works for Lighting Poles of Street Lighting Network-[Road 10]-[SW-3]	18	25-Oct-26	14-Nov-26	14-Dec-25	03-Jan-26	0%	25,126	25,126
CO-R10.S03-ES-S	Installation Works for Lighting Fixtures With Drop Wire of Street Lighting Network-[Road 10]-[SW-3]	18	31-Oct-26	19-Nov-26	26-Jan-26	16-Feb-26	0%	14,376	14,376
CO-R10.S03-ES-S	Backfilling Works for Lighting Poles of Street Lighting Network-[Road 10]-[SW-3]	12	01-Nov-26	14-Nov-26	27-Jan-26	10-Feb-26	0%	9,137	9,137
CO-R10.S03-ES-	Testing Works for Lighting Poles of Street Lighting Network-[Road 10]-[SW-3]	5	15-Nov-26	19-Nov-26	10-Feb-26	16-Feb-26	0%	9,137	9,137
Cabling Works		30	15-Nov-26	19-Dec-26	04-Jan-26	07-Feb-26	0%	47,398	47,398
CO-R10.S03-ES-S	Trench Excavation and Bedding Works for Street Lighting Network-[Road 10]-[SW-3]	10	15-Nov-26	25-Nov-26	04-Jan-26	14-Jan-26	0%	0	0
CO-R10.S03-ES-	Cable Laying Works for Street Lighting Network-[Road 10]-[SW-3]	10	26-Nov-26	07-Dec-26	15-Jan-26	26-Jan-26	0%	44,013	44,013
CO-R10.S03-ES-S	Trench Backfilling and Compaction Works for Street Lighting Network-[Road 10]-[SW-3]	10	08-Dec-26	19-Dec-26	27-Jan-26	07-Feb-26	0%	3,386	3,386
Distrubution Panel Boards		21	12-Apr-27	05-May-27	06-Jun-26	29-Jun-26	0%	282,560	282,560
CO-R10.S03-ES-S	Foundation Excavation Works For Panel Boards of Street Lighting Network-[Road 10]-[SW-3]	12	12-Apr-27	25-Apr-27	06-Jun-26	18-Jun-26	0%	21,647	21,647
CO-R10.S03-ES-S	Installation Works for Panel Board Concrete Foundations of Street Lighting Network-[Road 10]-[SW-3]	12	19-Apr-27	02-May-27	13-Jun-26	25-Jun-26	0%	48,506	48,506
CO-R10.S03-ES-S	A wall of concrete blocks to install the KWH meter of Street Lighting Network-[Road 10]-[SW-3]	12	19-Apr-27	02-May-27	13-Jun-26	25-Jun-26	0%	34,551	34,551
CO-R10.S03-ES-S	Installation Works for Lighting Panel Boards of Street Lighting Network-[Road 10]-[SW-3]	12	22-Apr-27	05-May-27	16-Jun-26	29-Jun-26	0%	177,856	177,856
Telecom Network		28	08-Dec-26	09-Jan-27	27-Jan-26	28-Feb-26	0%	80,545	80,545
Ducts Works		28	08-Dec-26	09-Jan-27	27-Jan-26	28-Feb-26	0%	66,431	66,431
CO-R10.S03-ES-TI	Trench Excavation and Bedding Works for Ducts of Telecom Network-[Road 10]-[SW-3]	7	08-Dec-26	15-Dec-26	27-Jan-26	03-Feb-26	0%	6,700	6,700
CO-R10.S03-ES-	Pipes Laying Works for Ducts of Telecom Network-[Road 10]-[SW-3]	7	16-Dec-26	23-Dec-26	04-Feb-26	11-Feb-26	0%	39,765	39,765
CO-R10.S03-ES-	Pouring Plain Concrete Above Ducts of Telecom Network-[Road 10]-[SW-3]	7	24-Dec-26	31-Dec-26	12-Feb-26	19-Feb-26	0%	6,700	6,700
CO-R10.S03-ES-TI	Trench Backfilling and Compaction Works for Ducts of Telecom Network-[Road 10]-[SW-3]	7	02-Jan-27	09-Jan-27	21-Feb-26	28-Feb-26	0%	13,266	13,266
Manholes Works		21	16-Dec-26	09-Jan-27	04-Feb-26	28-Feb-26	0%	14,114	14,114
CO-R10.S03-ES-	Excavation Works for Manholes of Telecom Network-[Road 10]-[SW-3]	7	16-Dec-26	23-Dec-26	04-Feb-26	11-Feb-26	0%	2,200	2,200
CO-R10.S03-ES-	Installation Works for Manholes of Telecom Network-[Road 10]-[SW-3]	7	24-Dec-26	31-Dec-26	12-Feb-26	19-Feb-26	0%	9,715	9,715
CO-R10.S03-ES-	Backfilling Works for Manholes of Telecom Network-[Road 10]-[SW-3]	7	02-Jan-27	09-Jan-27	21-Feb-26	28-Feb-26	0%	2,200	2,200
Road Works		118	25-Aug-26 A	11-Jul-27	07-Mar-26	29-Sep-26	9.68%	553,581	553,581
Pre-Bituminous Construction		21	10-Jan-27	02-Feb-27	07-Mar-26	02-Apr-26	0%	446,397	446,397
CO-R10.S03-ES-	Capping and Subgrade Layer for Road Works-[Road 10]-[SW-3]	18	10-Jan-27	30-Jan-27	07-Mar-26	30-Mar-26	0%	263,121	263,121
CO-R10.S03-ES-	Aggregate Base Course Layer for Road Works-[Road 10]-[SW-3]	18	13-Jan-27	02-Feb-27	10-Mar-26	02-Apr-26	0%	183,277	183,277
Pavement Works		10	25-Aug-26 A	11-Jul-27	17-Sep-26	29-Sep-26	50%	107,184	107,184
CO-R10.S03-ES-	Fixing of Interlock Tiles for Sidewalks Pavement-[Road 10]-[SW-3]	10	25-Aug-26 A	11-Jul-27	17-Sep-26	29-Sep-26	50%	107,184	107,184
SW_3-West		193	25-Aug-26 A	11-Jul-27	05-Jan-26	29-Sep-26	5.65%	948,532	948,532
Potable Water Network		16	13-Oct-26	31-Oct-26	05-Jan-26	25-Jan-26	0%	142,020	142,020

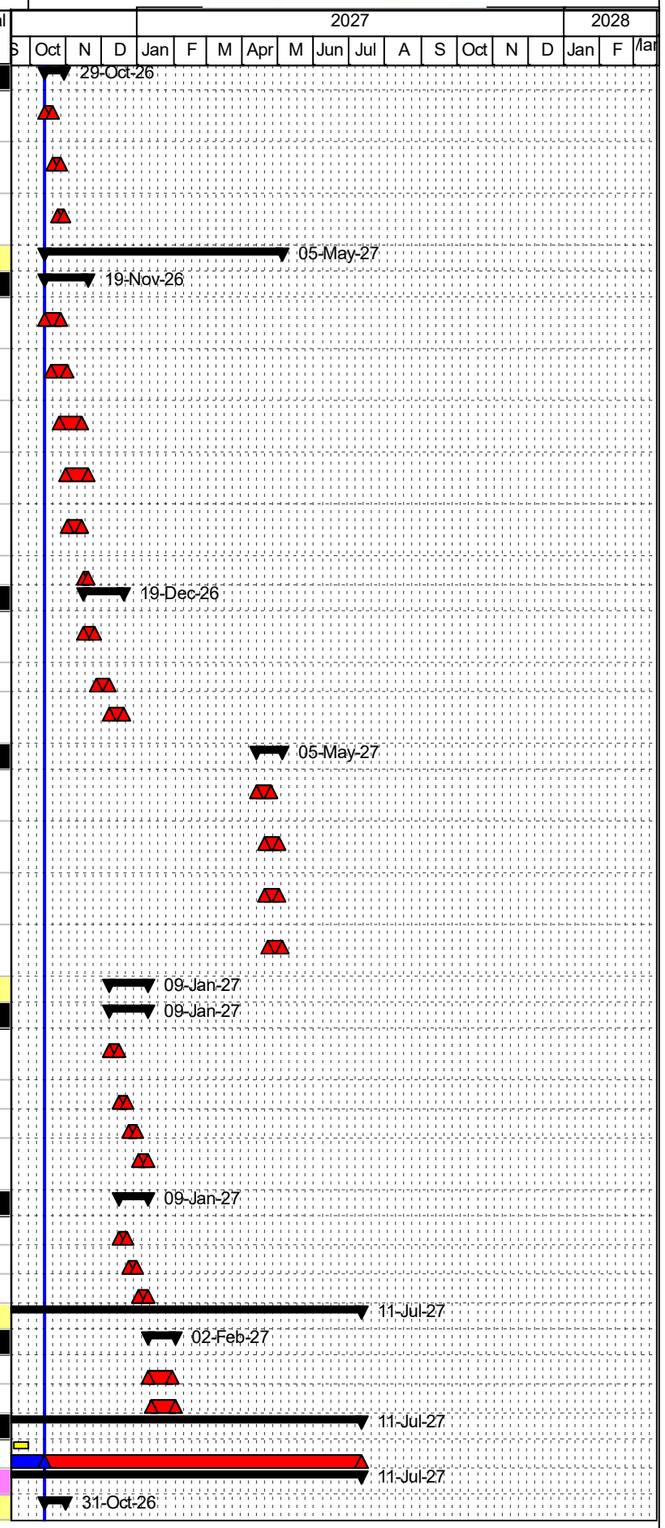

Primary Baseline
Remaining Work
Critical Remaining Work
Actual Work
Baseline Milestone
Milestone
Summary

Date	Revision	Checked	Approved
13-Oct-26	Third Industrial City		


Activity ID	Activity Name	Original Duration	Start	Finish	BL Project Start	BL Project Finish	Performance % Complete	Budgeted Total Cost	Remaining Total Cost
Valve Chamber		16	13-Oct-26	31-Oct-26	05-Jan-26	22-Jan-26	0%	85,213	85,213
CO-R10.S03-WE-F	Excavation Works for Main Line Valves and Valve Chambers of Potable Water Network-[Road 10]-[SW-3]	1	13-Oct-26	13-Oct-26	05-Jan-26	05-Jan-26	0%	4,352	4,352
CO-R10.S03-WE-F	RC Footing Works for Main Line Valves and Valve Chambers of Potable Water Network-[Road 10]-[SW-3]	3	14-Oct-26	17-Oct-26	06-Jan-26	08-Jan-26	0%	6,529	6,529
CO-R10.S03-WE-F	RC Wall Works for Main Line Valves and Valve Chambers of Potable Water Network-[Road 10]-[SW-3]	6	18-Oct-26	24-Oct-26	10-Jan-26	15-Jan-26	0%	15,234	15,234
CO-R10.S03-WE-F	RC Slab Works for Main Line Valves and Valve Chambers of Potable Water Network-[Road 10]-[SW-3]	2	25-Oct-26	26-Oct-26	17-Jan-26	18-Jan-26	0%	8,705	8,705
CO-R10.S03-WE-F	Insulation Works for Main Line Valves and Valve Chambers of Potable Water Network-[Road 10]-[SW-3]	1	27-Oct-26	27-Oct-26	19-Jan-26	19-Jan-26	0%	41,688	41,688
CO-R10.S03-WE-F	Backfilling Works for Main Line Valves and Valve Chambers of Potable Water Network-[Road 10]-[SW-3]	3	28-Oct-26	31-Oct-26	20-Jan-26	22-Jan-26	0%	8,705	8,705
Fire Hydrant		15	13-Oct-26	29-Oct-26	08-Jan-26	25-Jan-26	0%	56,808	56,808
CO-R10.S03-WE-F	Excavation Works for Fire Hydrants of Potable Water Network-[Road 10]-[SW-3]	6	13-Oct-26	19-Oct-26	08-Jan-26	14-Jan-26	0%	8,521	8,521
CO-R10.S03-WE-F	Installation Works for Fire Hydrant of Potable Water Network-[Road 10]-[SW-3]	6	20-Oct-26	26-Oct-26	15-Jan-26	21-Jan-26	0%	36,925	36,925
CO-R10.S03-WE-F	Trench Backfilling and Compaction Works for Fire Hydrants of Potable Water Network-[Road 10]-[SW-3]	6	24-Oct-26	29-Oct-26	19-Jan-26	25-Jan-26	0%	11,362	11,362
Street Lighting Network		172	13-Oct-26	05-May-27	22-Feb-26	29-Jun-26	0%	172,386	172,386
Lighting Poles Works		33	13-Oct-26	19-Nov-26	22-Feb-26	04-Apr-26	0%	68,790	68,790
CO-R10.S03-WE-S	Foundation Excavation Works for Lighting Poles of Street Lighting Network-[Road 10]-[SW-3]	12	13-Oct-26	26-Oct-26	22-Feb-26	07-Mar-26	0%	2,284	2,284
CO-R10.S03-WE-S	Installation Works for Lighting Poles Foundation of Street Lighting Network-[Road 10]-[SW-3]	12	19-Oct-26	01-Nov-26	28-Feb-26	12-Mar-26	0%	8,731	8,731
CO-R10.S03-WE-S	Installation Works for Lighting Poles of Street Lighting Network-[Road 10]-[SW-3]	18	25-Oct-26	14-Nov-26	05-Mar-26	29-Mar-26	0%	25,126	25,126
CO-R10.S03-WE-S	Installation Works for Lighting Fixtures With Drop Wire of Street Lighting Network-[Road 10]-[SW-3]	18	31-Oct-26	19-Nov-26	11-Mar-26	04-Apr-26	0%	14,376	14,376
CO-R10.S03-WE-S	Backfilling Works for Lighting Poles of Street Lighting Network-[Road 10]-[SW-3]	12	01-Nov-26	14-Nov-26	12-Mar-26	29-Mar-26	0%	9,137	9,137
CO-R10.S03-WE	Testing Works for Lighting Poles of Street Lighting Network-[Road 10]-[SW-3]	5	15-Nov-26	19-Nov-26	30-Mar-26	04-Apr-26	0%	9,137	9,137
Cabling Works		30	15-Nov-26	19-Dec-26	30-Mar-26	03-May-26	0%	47,398	47,398
CO-R10.S03-WE-S	Trench Excavation and Bedding Works for Street Lighting Network-[Road 10]-[SW-3]	10	15-Nov-26	25-Nov-26	30-Mar-26	09-Apr-26	0%	0	0
CO-R10.S03-WE	Cable Laying Works for Street Lighting Network-[Road 10]-[SW-3]	10	26-Nov-26	07-Dec-26	11-Apr-26	21-Apr-26	0%	44,013	44,013
CO-R10.S03-WE-S	Trench Backfilling and Compaction Works for Street Lighting Network-[Road 10]-[SW-3]	10	08-Dec-26	19-Dec-26	22-Apr-26	03-May-26	0%	3,386	3,386
Distrubution Panel Boards		21	12-Apr-27	05-May-27	06-Jun-26	29-Jun-26	0%	56,197	56,197
CO-R10.S03-WE-S	Foundation Excavation Works For Panel Boards of Street Lighting Network-[Road 10]-[SW-3]	12	12-Apr-27	25-Apr-27	06-Jun-26	18-Jun-26	0%	21,647	21,647
CO-R10.S03-WE-S	Installation Works for Panel Board Concrete Foundations of Street Lighting Network-[Road 10]-[SW-3]	12	19-Apr-27	02-May-27	13-Jun-26	25-Jun-26	0%	0	0
CO-R10.S03-WE-S	A wall of concrete blocks to install the KWH meter of Street Lighting Network-[Road 10]-[SW-3]	12	19-Apr-27	02-May-27	13-Jun-26	25-Jun-26	0%	34,551	34,551
CO-R10.S03-WE-S	Installation Works for Lighting Panel Boards of Street Lighting Network-[Road 10]-[SW-3]	12	22-Apr-27	05-May-27	16-Jun-26	29-Jun-26	0%	0	0
Telecom Network		24	08-Dec-26	04-Jan-27	17-Jun-26	14-Jul-26	0%	80,545	80,545
Ducts Works		24	08-Dec-26	04-Jan-27	17-Jun-26	14-Jul-26	0%	66,431	66,431
CO-R10.S03-WE-T	Trench Excavation and Bedding Works for Ducts of Telecom Network-[Road 10]-[SW-3]	3	08-Dec-26	10-Dec-26	17-Jun-26	20-Jun-26	0%	6,700	6,700
CO-R10.S03-WE	Pipes Laying Works for Ducts of Telecom Network-[Road 10]-[SW-3]	7	12-Dec-26	19-Dec-26	21-Jun-26	28-Jun-26	0%	39,765	39,765
CO-R10.S03-WE	Pouring Plain Concrete Above Ducts of Telecom Network-[Road 10]-[SW-3]	7	20-Dec-26	27-Dec-26	29-Jun-26	06-Jul-26	0%	6,700	6,700
CO-R10.S03-WE-T	Trench Backfilling and Compaction Works for Ducts of Telecom Network-[Road 10]-[SW-3]	7	28-Dec-26	04-Jan-27	07-Jul-26	14-Jul-26	0%	13,266	13,266

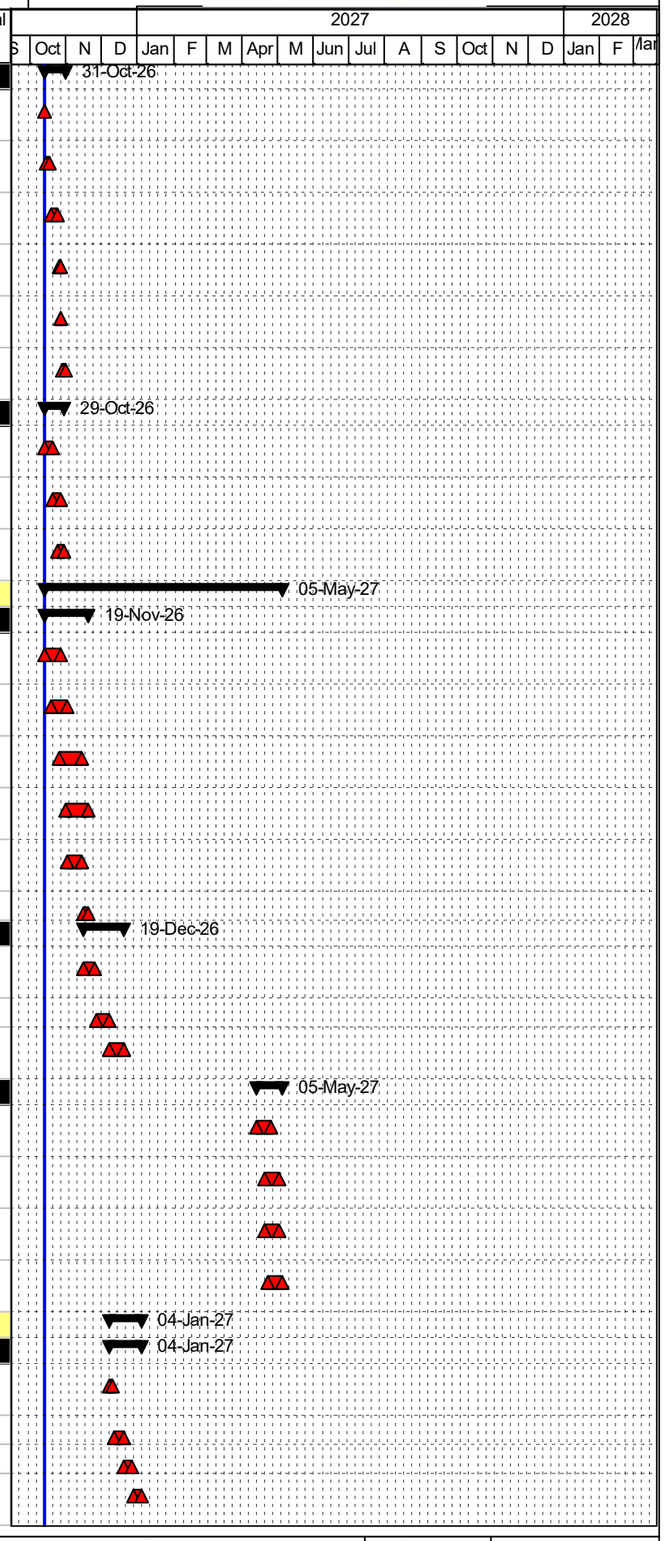

Primary Baseline
Actual Work
Summary
Remaining Work
Baseline Milestone
Critical Remaining Work
Milestone

Date	Revision	Checked	Approved
13-Oct-26	Third Industrial City		


Activity ID	Activity Name	Original Duration	Start	Finish	BL Project Start	BL Project Finish	Performance % Complete	Budgeted Total Cost	Remaining Total Cost
Manholes Works		21	12-Dec-26	04-Jan-27	21-Jun-26	14-Jul-26	0%	14,114	14,114
CO-R10.S03-WE	Excavation Works for Manholes of Telecom Network-[Road 10]-[SW-3]	7	12-Dec-26	19-Dec-26	21-Jun-26	28-Jun-26	0%	2,200	2,200
CO-R10.S03-WE	Installation Works for Manholes of Telecom Network-[Road 10]-[SW-3]	7	20-Dec-26	27-Dec-26	29-Jun-26	06-Jul-26	0%	9,715	9,715
CO-R10.S03-WE	Backfilling Works for Manholes of Telecom Network-[Road 10]-[SW-3]	7	28-Dec-26	04-Jan-27	07-Jul-26	14-Jul-26	0%	2,200	2,200
Road Works		114	25-Aug-26 A	11-Jul-27	21-Jul-26	29-Sep-26	9.68%	553,581	553,581
Pre-Bituminous Construction		21	05-Jan-27	28-Jan-27	21-Jul-26	13-Aug-26	0%	446,397	446,397
CO-R10.S03-WE	Capping and Subgrade Layer for Road Works-[Road 10]-[SW-3]	12	05-Jan-27	18-Jan-27	21-Jul-26	03-Aug-26	0%	263,121	263,121
CO-R10.S03-WE	Aggregate Base Course Layer for Road Works-[Road 10]-[SW-3]	18	09-Jan-27	28-Jan-27	25-Jul-26	13-Aug-26	0%	183,277	183,277
Pavement Works		10	25-Aug-26 A	11-Jul-27	17-Sep-26	29-Sep-26	50%	107,184	107,184
CO-R10.S03-WE	Fixing of Interlock Tiles for Sidewalks Pavement-[Road 10]-[SW-3]	10	25-Aug-26 A	11-Jul-27	17-Sep-26	29-Sep-26	50%	107,184	107,184
SW-4		417	17-Jun-26 A	11-Jul-27	23-Jul-25	01-Oct-26	20.64%	2,715,775	2,647,472
SW_4-East		351	21-Jun-26 A	11-Jul-27	23-Jul-25	29-Sep-26	19.39%	1,264,471	1,264,471
Sewage Network		1	13-Oct-26	13-Oct-26	23-Jul-25	23-Jul-25	0%	8,813	8,813
Manholes		1	13-Oct-26	13-Oct-26	23-Jul-25	23-Jul-25	0%	8,813	8,813
CO-R10.S04-ES-	Testing Works for Main Line Manholes of Sewage Network-[Road 10]-[SW-4]	1	13-Oct-26	13-Oct-26	23-Jul-25	23-Jul-25	0%	8,813	8,813
Storm Drainage Network		10	13-Oct-26	24-Oct-26	18-Dec-25	22-Jan-26	0%	34,251	34,251
Manholes		1	13-Oct-26	13-Oct-26	18-Dec-25	18-Dec-25	0%	20,352	20,352
CO-R10.S04-ES-	Testing Works for Manholes of Storm Drainage Network-[Road 10]-[SW-4]	1	13-Oct-26	13-Oct-26	18-Dec-25	18-Dec-25	0%	20,352	20,352
Catch Basin Sections		10	13-Oct-26	24-Oct-26	12-Jan-26	22-Jan-26	0%	13,899	13,899
CO-R10.S04-ES-	Testing Works for Catch Basins of Storm Drainage Network-[Road 10]-[SW-4]	10	13-Oct-26	24-Oct-26	12-Jan-26	22-Jan-26	0%	13,899	13,899
Potable Water Network		234	21-Jun-26 A	07-Nov-26	15-Jan-26	11-Feb-26	42.42%	451,664	451,664
Valve Chamber		227	21-Jun-26 A	29-Oct-26	15-Jan-26	02-Feb-26	42.42%	451,664	451,664
CO-R10.S04-ES-P	Insulation Works for Main Line Valves and Valve Chambers of Potable Water Network-[Road 10]-[SW-4]	1	21-Jun-26 A	26-Oct-26	29-Jan-26	29-Jan-26	60%	319,299	319,299
CO-R10.S04-ES-P	Excavation Works for Main Line Valves and Valve Chambers of Potable Water Network-[Road 10]-[SW-4]	1	13-Oct-26	13-Oct-26	15-Jan-26	15-Jan-26	0%	16,109	16,109
CO-R10.S04-ES-P	RC Footing Works for Main Line Valves and Valve Chambers of Potable Water Network-[Road 10]-[SW-4]	3	14-Oct-26	17-Oct-26	17-Jan-26	19-Jan-26	0%	19,376	19,376
CO-R10.S04-ES-P	RC Wall Works for Main Line Valves and Valve Chambers of Potable Water Network-[Road 10]-[SW-4]	6	18-Oct-26	24-Oct-26	20-Jan-26	26-Jan-26	0%	45,211	45,211
CO-R10.S04-ES-P	RC Slab Works for Main Line Valves and Valve Chambers of Potable Water Network-[Road 10]-[SW-4]	2	25-Oct-26	26-Oct-26	27-Jan-26	28-Jan-26	0%	25,835	25,835
CO-R10.S04-ES-P	Backfilling Works for Main Line Valves and Valve Chambers of Potable Water Network-[Road 10]-[SW-4]	3	27-Oct-26	29-Oct-26	31-Jan-26	02-Feb-26	0%	25,835	25,835
Fire Hydrant		21	14-Oct-26	07-Nov-26	19-Jan-26	11-Feb-26	0%	0	0
CO-R10.S04-ES-P	Excavation Works for Fire Hydrants of Potable Water Network-[Road 10]-[SW-4]	7	14-Oct-26	21-Oct-26	19-Jan-26	26-Jan-26	0%	0	0
CO-R10.S04-ES-P	Installation Works for Fire Hydrant of Potable Water Network-[Road 10]-[SW-4]	7	22-Oct-26	29-Oct-26	27-Jan-26	03-Feb-26	0%	0	0
CO-R10.S04-ES-P	Trench Backfilling and Compaction Works for Fire Hydrants of Potable Water Network-[Road 10]-[SW-4]	7	31-Oct-26	07-Nov-26	04-Feb-26	11-Feb-26	0%	0	0
Street Lighting Network		139	13-Oct-26	28-Mar-27	10-Mar-26	15-Jun-26	0%	135,616	135,616
Lighting Poles Works		139	13-Oct-26	28-Mar-27	10-Mar-26	20-Apr-26	0%	68,790	68,790
CO-R10.S04-ES-S	Foundation Excavation Works for Lighting Poles of Street Lighting Network-[Road 10]-[SW-4]	7	13-Oct-26	20-Oct-26	10-Mar-26	17-Mar-26	0%	2,284	2,284
CO-R10.S04-ES-S	Installation Works for Lighting Poles Foundation of Street Lighting Network-[Road 10]-[SW-4]	7	19-Oct-26	26-Oct-26	16-Mar-26	26-Mar-26	0%	8,731	8,731
CO-R10.S04-ES-S	Installation Works for Lighting Poles of Street Lighting Network-[Road 10]-[SW-4]	7	25-Oct-26	01-Nov-26	25-Mar-26	01-Apr-26	0%	25,126	25,126
CO-R10.S04-ES-S	Backfilling Works for Lighting Poles of Street Lighting Network-[Road 10]-[SW-4]	15	15-Nov-26	01-Dec-26	25-Mar-26	11-Apr-26	0%	9,137	9,137
CO-R10.S04-ES-	Testing Works for Lighting Poles of Street Lighting Network-[Road 10]-[SW-4]	7	02-Dec-26	09-Dec-26	12-Apr-26	19-Apr-26	0%	9,137	9,137
CO-R10.S04-ES-S	Installation Works for Lighting Fixtures With Drop Wire of Street Lighting Network-[Road 10]-[SW-4]	18	04-Mar-27	28-Mar-27	31-Mar-26	20-Apr-26	0%	14,376	14,376
Cabling Works		21	02-Nov-26	25-Nov-26	02-Apr-26	26-Apr-26	0%	47,398	47,398

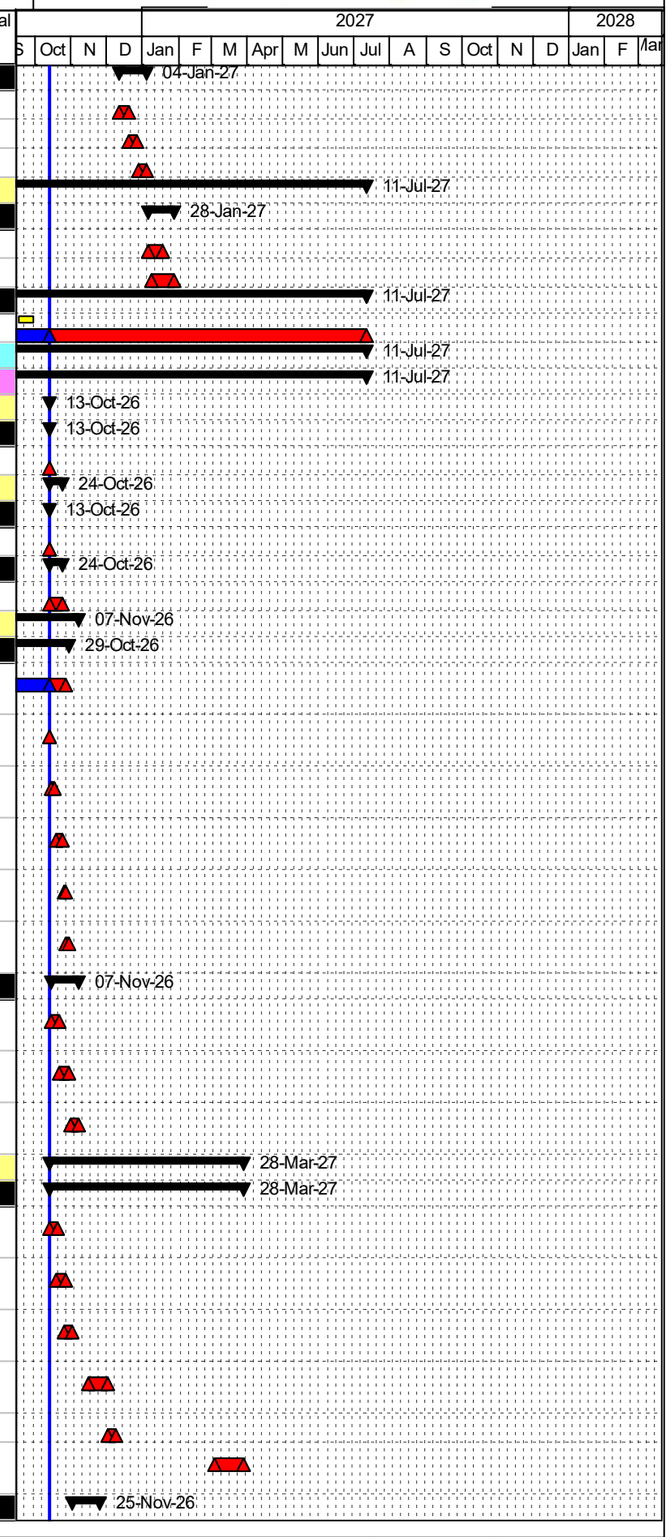

Primary Baseline · Actual Work · Summary
Remaining Work · Baseline Milestone
Critical Remaining Work · Milestone

Date	Revision	Checked	Approved
13-Oct-26	Third Industrial City		


Activity ID	Activity Name	Original Duration	Start	Finish	BL Project Start	BL Project Finish	Performance % Complete	Budgeted Total Cost	Remaining Total Cost
CO-R10.S04-ES-S	Trench Excavation and Bedding Works for Street Lighting Network-[Road 10]-[SW-4]	7	02-Nov-26	09-Nov-26	02-Apr-26	09-Apr-26	0%	0	0
CO-R10.S04-ES-	Cable Laying Works for Street Lighting Network-[Road 10]-[SW-4]	7	10-Nov-26	17-Nov-26	11-Apr-26	18-Apr-26	0%	44,013	44,013
CO-R10.S04-ES-S	Trench Backfilling and Compaction Works for Street Lighting Network-[Road 10]-[SW-4]	7	18-Nov-26	25-Nov-26	19-Apr-26	26-Apr-26	0%	3,386	3,386
Distrubution Panel Boards		39	26-Nov-26	10-Jan-27	27-Apr-26	15-Jun-26	0%	19,427	19,427
CO-R10.S04-ES-S	Foundation Excavation Works For Panel Boards of Street Lighting Network-[Road 10]-[SW-4]	18	26-Nov-26	16-Dec-26	27-Apr-26	17-May-26	0%	0	0
CO-R10.S04-ES-S	Installation Works for Panel Board Concrete Foundations of Street Lighting Network-[Road 10]-[SW-4]	12	07-Dec-26	20-Dec-26	07-May-26	20-May-26	0%	0	0
CO-R10.S04-ES-S	Installation Works for Lighting Panel Boards of Street Lighting Network-[Road 10]-[SW-4]	12	21-Dec-26	03-Jan-27	21-May-26	08-Jun-26	0%	0	0
CO-R10.S04-ES-S	A wall of concrete blocks to install the KWH meter of Street Lighting Network-[Road 10]-[SW-4]	18	21-Dec-26	10-Jan-27	21-May-26	15-Jun-26	0%	19,427	19,427
Telecom Network		28	16-Dec-26	17-Jan-27	25-Apr-26	22-Jul-26	0%	80,545	80,545
Ducts Works		28	16-Dec-26	17-Jan-27	25-Apr-26	31-May-26	0%	66,431	66,431
CO-R10.S04-ES-TI	Trench Excavation and Bedding Works for Ducts of Telecom Network-[Road 10]-[SW-4]	7	16-Dec-26	23-Dec-26	25-Apr-26	02-May-26	0%	6,700	6,700
CO-R10.S04-ES-	Pipes Laying Works for Ducts of Telecom Network-[Road 10]-[SW-4]	7	24-Dec-26	31-Dec-26	03-May-26	10-May-26	0%	39,765	39,765
CO-R10.S04-ES-	Pouring Plain Concrete Above Ducts of Telecom Network-[Road 10]-[SW-4]	7	02-Jan-27	09-Jan-27	11-May-26	18-May-26	0%	6,700	6,700
CO-R10.S04-ES-TI	Trench Backfilling and Compaction Works for Ducts of Telecom Network-[Road 10]-[SW-4]	7	10-Jan-27	17-Jan-27	19-May-26	31-May-26	0%	13,266	13,266
Manholes Works		21	24-Dec-26	17-Jan-27	29-Jun-26	22-Jul-26	0%	14,114	14,114
CO-R10.S04-ES-	Excavation Works for Manholes of Telecom Network-[Road 10]-[SW-4]	7	24-Dec-26	31-Dec-26	29-Jun-26	06-Jul-26	0%	2,200	2,200
CO-R10.S04-ES-	Installation Works for Manholes of Telecom Network-[Road 10]-[SW-4]	7	02-Jan-27	09-Jan-27	07-Jul-26	14-Jul-26	0%	9,715	9,715
CO-R10.S04-ES-	Backfilling Works for Manholes of Telecom Network-[Road 10]-[SW-4]	7	10-Jan-27	17-Jan-27	15-Jul-26	22-Jul-26	0%	2,200	2,200
Road Works		121	25-Aug-26 A	11-Jul-27	23-Jul-26	29-Sep-26	9.68%	553,581	553,581
Pre-Bituminous Construction		17	18-Jan-27	06-Feb-27	23-Jul-26	11-Aug-26	0%	446,397	446,397
CO-R10.S04-ES-	Capping and Subgrade Layer for Road Works-[Road 10]-[SW-4]	14	18-Jan-27	02-Feb-27	23-Jul-26	08-Aug-26	0%	263,121	263,121
CO-R10.S04-ES-	Aggregate Base Course Layer for Road Works-[Road 10]-[SW-4]	12	24-Jan-27	06-Feb-27	29-Jul-26	11-Aug-26	0%	183,277	183,277
Pavement Works		10	25-Aug-26 A	11-Jul-27	17-Sep-26	29-Sep-26	50%	107,184	107,184
CO-R10.S04-ES-	Fixing of Interlock Tiles for Sidewalks Pavement-[Road 10]-[SW-4]	10	25-Aug-26 A	11-Jul-27	17-Sep-26	29-Sep-26	50%	107,184	107,184
SW_4-West		417	17-Jun-26 A	11-Jul-27	11-Nov-25	01-Oct-26	21.73%	1,451,304	1,383,001
Sewage Network		1	13-Oct-26	13-Oct-26	11-Nov-25	11-Nov-25	0%	10,264	10,264
Manholes		1	13-Oct-26	13-Oct-26	11-Nov-25	11-Nov-25	0%	10,264	10,264
CO-R10.S04-WE	Testing Works for Main Line Manholes of Sewage Network-[Road 10]-[SW-4]	1	13-Oct-26	13-Oct-26	11-Nov-25	11-Nov-25	0%	10,264	10,264
Storm Drainage Network		247	17-Jun-26 A	20-Oct-26	18-Dec-25	26-Jan-26	47.71%	147,127	78,825
Manholes		1	13-Oct-26	13-Oct-26	18-Dec-25	18-Dec-25	0%	22,038	22,038
CO-R10.S04-WE	Testing Works for Manholes of Storm Drainage Network-[Road 10]-[SW-4]	1	13-Oct-26	13-Oct-26	18-Dec-25	18-Dec-25	0%	22,038	22,038
Catch Basin Sections		247	17-Jun-26 A	20-Oct-26	28-Dec-25	26-Jan-26	56.11%	125,090	56,787
CO-R10.S04-WE-S	Trench Excavation and Bedding Works for Catch Basins of Storm Drainage Network-[Road 10]-[SW-4]	6	17-Jun-26 A	14-Oct-26	28-Dec-25	03-Jan-26	80%	20,848	6,949
CO-R10.S04-WE-S	Installation and Pipes Laying Connection Works for Catch Basins of Storm Drainage Network-[Road 10]-[SW-4]	7	20-Jun-26 A	14-Oct-26	04-Jan-26	11-Jan-26	70%	62,545	17,870
CO-R10.S04-WE	Testing Works for Catch Basins of Storm Drainage Network-[Road 10]-[SW-4]	10	23-Jun-26 A	15-Oct-26	12-Jan-26	22-Jan-26	70%	13,899	4,170
CO-R10.S04-WE-S	Trench Backfilling and Compaction Works for Catch Basins of Storm Drainage Network-[Road 10]-[SW-4]	7	13-Oct-26	20-Oct-26	19-Jan-26	26-Jan-26	0%	27,798	27,798
Potable Water Network		234	21-Jun-26 A	07-Nov-26	15-Jan-26	11-Feb-26	47.18%	406,090	406,090
Valve Chamber		227	21-Jun-26 A	29-Oct-26	15-Jan-26	02-Feb-26	47.18%	406,090	406,090
CO-R10.S04-WE-F	Insulation Works for Main Line Valves and Valve Chambers of Potable Water Network-[Road 10]-[SW-4]	1	21-Jun-26 A	26-Oct-26	29-Jan-26	29-Jan-26	60%	319,299	319,299
CO-R10.S04-WE-F	Excavation Works for Main Line Valves and Valve Chambers of Potable Water Network-[Road 10]-[SW-4]	1	13-Oct-26	13-Oct-26	15-Jan-26	15-Jan-26	0%	8,679	8,679
CO-R10.S04-WE-F	RC Footing Works for Main Line Valves and Valve Chambers of Potable Water Network-[Road 10]-[SW-4]	3	14-Oct-26	17-Oct-26	17-Jan-26	19-Jan-26	0%	13,019	13,019

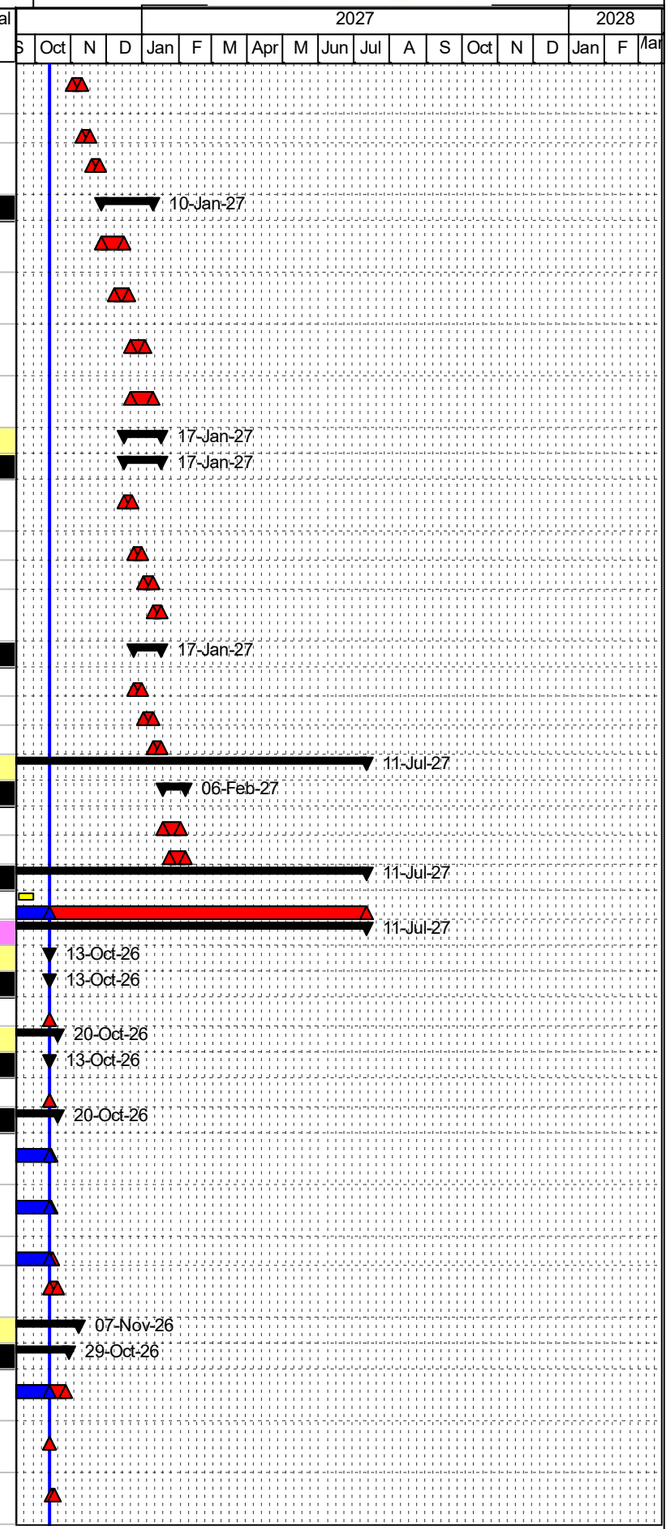

Primary Baseline
Actual Work
Summary
Remaining Work
Baseline Milestone
Critical Remaining Work
Milestone

Date	Revision	Checked	Approved
13-Oct-26	Third Industrial City		


Activity ID	Activity Name	Original Duration	Start	Finish	BL Project Start	BL Project Finish	Performance % Complete	Budgeted Total Cost	Remaining Total Cost
CO-R10.S04-WE-F	RC Wall Works for Main Line Valves and Valve Chambers of Potable Water Network-[Road 10]-[SW-4]	6	18-Oct-26	24-Oct-26	20-Jan-26	26-Jan-26	0%	30,377	30,377
CO-R10.S04-WE-F	RC Slab Works for Main Line Valves and Valve Chambers of Potable Water Network-[Road 10]-[SW-4]	2	25-Oct-26	26-Oct-26	27-Jan-26	28-Jan-26	0%	17,358	17,358
CO-R10.S04-WE-F	Backfilling Works for Main Line Valves and Valve Chambers of Potable Water Network-[Road 10]-[SW-4]	3	27-Oct-26	29-Oct-26	31-Jan-26	02-Feb-26	0%	17,358	17,358
Fire Hydrant		21	14-Oct-26	07-Nov-26	19-Jan-26	11-Feb-26	0%	0	0
CO-R10.S04-WE-F	Excavation Works for Fire Hydrants of Potable Water Network-[Road 10]-[SW-4]	7	14-Oct-26	21-Oct-26	19-Jan-26	26-Jan-26	0%	0	0
CO-R10.S04-WE-F	Installation Works for Fire Hydrant of Potable Water Network-[Road 10]-[SW-4]	7	22-Oct-26	29-Oct-26	27-Jan-26	03-Feb-26	0%	0	0
CO-R10.S04-WE-F	Trench Backfilling and Compaction Works for Fire Hydrants of Potable Water Network-[Road 10]-[SW-4]	7	31-Oct-26	07-Nov-26	04-Feb-26	11-Feb-26	0%	0	0
Irrigation Network		71	21-Oct-26	11-Jan-27	12-Feb-26	08-Mar-26	0%	118,080	118,080
Main Line Pipes		71	21-Oct-26	11-Jan-27	12-Feb-26	08-Mar-26	0%	118,080	118,080
CO-R10.S04-WE-I	Trench Excavation and Bedding Works for Main Lines of Irrigation Network-[Road 10]-[SW-4]	6	21-Oct-26	27-Oct-26	12-Feb-26	18-Feb-26	0%	21,368	21,368
CO-R10.S04-WE	Pipes Laying Works for Main Lines of Irrigation Network-[Road 10]-[SW-4]	7	28-Oct-26	04-Nov-26	19-Feb-26	26-Feb-26	0%	64,103	64,103
CO-R10.S04-WE	Installation Works for Main Line Valves of Irrigation Network-[Road 10]-[SW-4]	3	03-Jan-27	05-Jan-27	28-Feb-26	02-Mar-26	0%	21,926	21,926
CO-R10.S04-WE-I	Trench Backfilling and Compaction Works for Main Lines of Irrigation Network-[Road 10]-[SW-4]	5	06-Jan-27	11-Jan-27	03-Mar-26	08-Mar-26	0%	10,684	10,684
Street Lighting Network		97	12-Jan-27	09-May-27	09-Mar-26	07-Jul-26	0%	135,616	135,616
Lighting Poles Works		61	12-Jan-27	28-Mar-27	09-Mar-26	23-Apr-26	0%	68,790	68,790
CO-R10.S04-WE-S	Foundation Excavation Works for Lighting Poles of Street Lighting Network-[Road 10]-[SW-4]	10	12-Jan-27	23-Jan-27	09-Mar-26	19-Mar-26	0%	2,284	2,284
CO-R10.S04-WE-S	Installation Works for Lighting Poles Foundation of Street Lighting Network-[Road 10]-[SW-4]	10	18-Jan-27	28-Jan-27	15-Mar-26	29-Mar-26	0%	8,731	8,731
CO-R10.S04-WE-S	Installation Works for Lighting Poles of Street Lighting Network-[Road 10]-[SW-4]	18	24-Jan-27	13-Feb-27	24-Mar-26	13-Apr-26	0%	25,126	25,126
CO-R10.S04-WE-S	Backfilling Works for Lighting Poles of Street Lighting Network-[Road 10]-[SW-4]	15	27-Jan-27	13-Feb-27	30-Mar-26	15-Apr-26	0%	9,137	9,137
CO-R10.S04-WE	Testing Works for Lighting Poles of Street Lighting Network-[Road 10]-[SW-4]	7	14-Feb-27	21-Feb-27	16-Apr-26	23-Apr-26	0%	9,137	9,137
CO-R10.S04-WE-S	Installation Works for Lighting Fixtures With Drop Wire of Street Lighting Network-[Road 10]-[SW-4]	18	04-Mar-27	28-Mar-27	04-Apr-26	23-Apr-26	0%	14,376	14,376
Cabling Works		30	14-Feb-27	24-Mar-27	14-Apr-26	18-May-26	0%	47,398	47,398
CO-R10.S04-WE-S	Trench Excavation and Bedding Works for Street Lighting Network-[Road 10]-[SW-4]	10	14-Feb-27	25-Feb-27	14-Apr-26	25-Apr-26	0%	0	0
CO-R10.S04-WE	Cable Laying Works for Street Lighting Network-[Road 10]-[SW-4]	10	27-Feb-27	13-Mar-27	26-Apr-26	06-May-26	0%	44,013	44,013
CO-R10.S04-WE-S	Trench Backfilling and Compaction Works for Street Lighting Network-[Road 10]-[SW-4]	10	14-Mar-27	24-Mar-27	07-May-26	18-May-26	0%	3,386	3,386
Distrubution Panel Boards		39	25-Mar-27	09-May-27	19-May-26	07-Jul-26	0%	19,427	19,427
CO-R10.S04-WE-S	Foundation Excavation Works For Panel Boards of Street Lighting Network-[Road 10]-[SW-4]	18	25-Mar-27	14-Apr-27	19-May-26	13-Jun-26	0%	0	0
CO-R10.S04-WE-S	Installation Works for Panel Board Concrete Foundations of Street Lighting Network-[Road 10]-[SW-4]	12	05-Apr-27	18-Apr-27	03-Jun-26	16-Jun-26	0%	0	0
CO-R10.S04-WE-S	Installation Works for Lighting Panel Boards of Street Lighting Network-[Road 10]-[SW-4]	12	19-Apr-27	02-May-27	17-Jun-26	30-Jun-26	0%	0	0
CO-R10.S04-WE-S	A wall of concrete blocks to install the KWH meter of Street Lighting Network-[Road 10]-[SW-4]	18	19-Apr-27	09-May-27	17-Jun-26	07-Jul-26	0%	19,427	19,427
Telecom Network		28	23-Mar-27	24-Apr-27	21-Jun-26	22-Jul-26	0%	80,545	80,545
Ducts Works		28	23-Mar-27	24-Apr-27	21-Jun-26	22-Jul-26	0%	66,431	66,431
CO-R10.S04-WE-T	Trench Excavation and Bedding Works for Ducts of Telecom Network-[Road 10]-[SW-4]	7	23-Mar-27	30-Mar-27	21-Jun-26	28-Jun-26	0%	6,700	6,700
CO-R10.S04-WE	Pipes Laying Works for Ducts of Telecom Network-[Road 10]-[SW-4]	7	31-Mar-27	07-Apr-27	29-Jun-26	06-Jul-26	0%	39,765	39,765
CO-R10.S04-WE	Pouring Plain Concrete Above Ducts of Telecom Network-[Road 10]-[SW-4]	7	08-Apr-27	15-Apr-27	07-Jul-26	14-Jul-26	0%	6,700	6,700

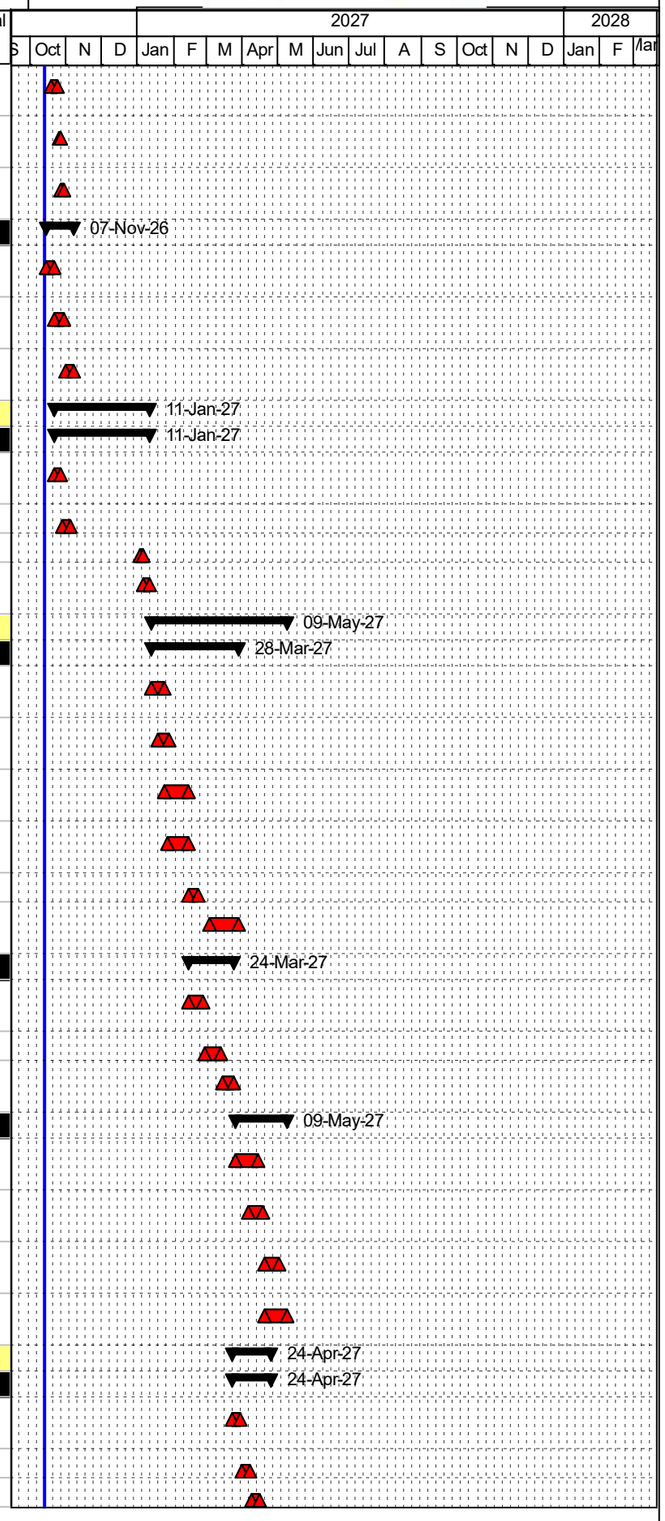

Primary Baseline
Remaining Work
Critical Remaining Work
Actual Work
Baseline Milestone
Milestone
Summary

Date	Revision	Checked	Approved
13-Oct-26	Third Industrial City		


Activity ID	Activity Name	Original Duration	Start	Finish	BL Project Start	BL Project Finish	Performance % Complete	Budgeted Total Cost	Remaining Total Cost
CO-R10.S04-WE-T	Trench Backfilling and Compaction Works for Ducts of Telecom Network-[Road 10]-[SW-4]	7	17-Apr-27	24-Apr-27	15-Jul-26	22-Jul-26	0%	13,266	13,266
Manholes Works		21	31-Mar-27	24-Apr-27	29-Jun-26	22-Jul-26	0%	14,114	14,114
CO-R10.S04-WE	Excavation Works for Manholes of Telecom Network-[Road 10]-[SW-4]	7	31-Mar-27	07-Apr-27	29-Jun-26	06-Jul-26	0%	2,200	2,200
CO-R10.S04-WE	Installation Works for Manholes of Telecom Network-[Road 10]-[SW-4]	7	08-Apr-27	15-Apr-27	07-Jul-26	14-Jul-26	0%	9,715	9,715
CO-R10.S04-WE	Backfilling Works for Manholes of Telecom Network-[Road 10]-[SW-4]	7	17-Apr-27	24-Apr-27	15-Jul-26	22-Jul-26	0%	2,200	2,200
Road Works		198	25-Aug-26 A	11-Jul-27	23-Jul-26	01-Oct-26	9.68%	553,581	553,581
Pre-Bituminous Construction		15	25-Apr-27	11-May-27	23-Jul-26	09-Aug-26	0%	446,397	446,397
CO-R10.S04-WE	Capping and Subgrade Layer for Road Works-[Road 10]-[SW-4]	12	25-Apr-27	08-May-27	23-Jul-26	05-Aug-26	0%	263,121	263,121
CO-R10.S04-WE	Aggregate Base Course Layer for Road Works-[Road 10]-[SW-4]	12	28-Apr-27	11-May-27	27-Jul-26	09-Aug-26	0%	183,277	183,277
Pavement Works		12	25-Aug-26 A	11-Jul-27	17-Sep-26	01-Oct-26	50%	107,184	107,184
CO-R10.S04-WE	Fixing of Interlock Tiles for Sidewalks Pavement-[Road 10]-[SW-4]	12	25-Aug-26 A	11-Jul-27	17-Sep-26	01-Oct-26	50%	107,184	107,184
Road 11 Local 1 (670 LM)		530	02-Apr-26 A	02-Aug-27	04-Oct-25	13-Oct-26	29.37%	425,006	387,595
SW_5		318	25-Apr-26 A	02-Aug-27	03-Jan-26	11-Oct-26	36.37%	157,859	120,448
Irrigation Network		245	25-Apr-26 A	24-Oct-26	03-Jan-26	21-Jan-26	30.45%	85,996	48,585
Main Line Pipes		245	25-Apr-26 A	24-Oct-26	03-Jan-26	21-Jan-26	30.45%	85,996	48,585
CO-R11.S05-IR-1	Pipes Laying Works for Main Lines of Irrigation Network-[Road 11]-[SW-5]	7	25-Apr-26 A	13-Oct-26	03-Jan-26	10-Jan-26	70%	37,411	0
CO-R11.S05-IR-1	Installation Works for Main Line Valves of Irrigation Network-[Road 11]-[SW-5]	3	13-Oct-26	15-Oct-26	11-Jan-26	13-Jan-26	0%	42,350	42,350
CO-R11.S05-IR-130	Trench Backfilling and Compaction Works for Main Lines of Irrigation Network-[Road 11]-[SW-5]	7	17-Oct-26	24-Oct-26	14-Jan-26	21-Jan-26	0%	6,235	6,235
Telecom Network		21	24-Dec-26	17-Jan-27	29-Jun-26	22-Jul-26	0%	9,401	9,401
Manholes Works		21	24-Dec-26	17-Jan-27	29-Jun-26	22-Jul-26	0%	9,401	9,401
CO-R11.S05-TE-1	Excavation Works for Manholes of Telecom Network-[Road 11]-[SW-5]	7	24-Dec-26	31-Dec-26	29-Jun-26	06-Jul-26	0%	1,257	1,257
CO-R11.S05-TE-1	Installation Works for Manholes of Telecom Network-[Road 11]-[SW-5]	7	02-Jan-27	09-Jan-27	07-Jul-26	14-Jul-26	0%	6,887	6,887
CO-R11.S05-TE-1	Backfilling Works for Manholes of Telecom Network-[Road 11]-[SW-5]	7	10-Jan-27	17-Jan-27	15-Jul-26	22-Jul-26	0%	1,257	1,257
Road Works		10	25-Aug-26 A	02-Aug-27	30-Sep-26	11-Oct-26	50%	62,462	62,462
Pavement Works		10	25-Aug-26 A	02-Aug-27	30-Sep-26	11-Oct-26	50%	62,462	62,462
CO-R11.S05-RD-F	Fixing of Interlock Tiles for Sidewalks Pavement-[Road 11]-[SW-5]	10	25-Aug-26 A	02-Aug-27	30-Sep-26	11-Oct-26	50%	62,462	62,462
SW_6		530	02-Apr-26 A	02-Aug-27	04-Oct-25	13-Oct-26	25.24%	267,147	267,147
Sewage Network		318	02-Apr-26 A	18-Oct-26	04-Oct-25	14-Oct-25	44.44%	81,435	81,435
Manholes		318	02-Apr-26 A	18-Oct-26	04-Oct-25	14-Oct-25	44.44%	81,435	81,435
CO-R11.S06-SW-18	Install Grp Liner Wall Works for Main Line Manholes of Sewage Network-[Road 11]-[SW-6]	4	02-Apr-26 A	17-Oct-26	04-Oct-25	07-Oct-25	50%	72,387	72,387
CO-R11.S06-SW-1	Testing Works for Main Line Manholes of Sewage Network-[Road 11]-[SW-6]	1	18-Oct-26	18-Oct-26	14-Oct-25	14-Oct-25	0%	9,048	9,048
Potable Water Network		177	13-Oct-26	11-May-27	28-Jan-26	28-Feb-26	0%	53,759	53,759
Valve Chamber		6	13-Oct-26	19-Oct-26	28-Jan-26	03-Feb-26	0%	15,887	15,887
CO-R11.S06-PW-21	Installation Works for Main Line Valves and Valve Chambers of Potable Water Network-[Road 11]-[SW-6]	6	13-Oct-26	19-Oct-26	28-Jan-26	03-Feb-26	0%	15,887	15,887
Fire Hydrant		21	18-Apr-27	11-May-27	04-Feb-26	28-Feb-26	0%	37,872	37,872
CO-R11.S06-PW-14	Excavation Works for Fire Hydrants of Potable Water Network-[Road 11]-[SW-6]	7	18-Apr-27	25-Apr-27	04-Feb-26	11-Feb-26	0%	5,681	5,681
CO-R11.S06-PW-15	Installation Works for Fire Hydrant of Potable Water Network-[Road 11]-[SW-6]	7	26-Apr-27	03-May-27	12-Feb-26	19-Feb-26	0%	24,617	24,617
CO-R11.S06-PW-16	Trench Backfilling and Compaction Works for Fire Hydrants of Potable Water Network-[Road 11]-[SW-6]	7	04-May-27	11-May-27	21-Feb-26	28-Feb-26	0%	7,574	7,574
Street Lighting Network		217	13-Oct-26	03-Jul-27	19-May-26	25-Jul-26	0%	60,090	60,090
Lighting Poles Works		217	13-Oct-26	03-Jul-27	24-Jun-26	19-Jul-26	0%	38,090	38,090
CO-R11.S06-SL-21(	Backfilling Works for Lighting Poles of Street Lighting Network-[Road 11]-[SW-6]	15	13-Oct-26	29-Oct-26	24-Jun-26	11-Jul-26	0%	10,659	10,659
CO-R11.S06-SL-2	Testing Works for Lighting Poles of Street Lighting Network-[Road 11]-[SW-6]	7	31-Oct-26	07-Nov-26	12-Jul-26	19-Jul-26	0%	10,659	10,659
CO-R11.S06-SL-13(	Installation Works for Lighting Fixtures With Drop Wire of Street Lighting Network-[Road 11]-[SW-6]	18	13-Jun-27	03-Jul-27	29-Jun-26	19-Jul-26	0%	16,771	16,771
Cabling Works		10	13-Oct-26	24-Oct-26	19-May-26	03-Jun-26	0%	3,989	3,989
CO-R11.S06-SL-16(	Trench Backfilling and Compaction Works for Street Lighting Network-[Road 11]-[SW-6]	10	13-Oct-26	24-Oct-26	19-May-26	03-Jun-26	0%	3,989	3,989

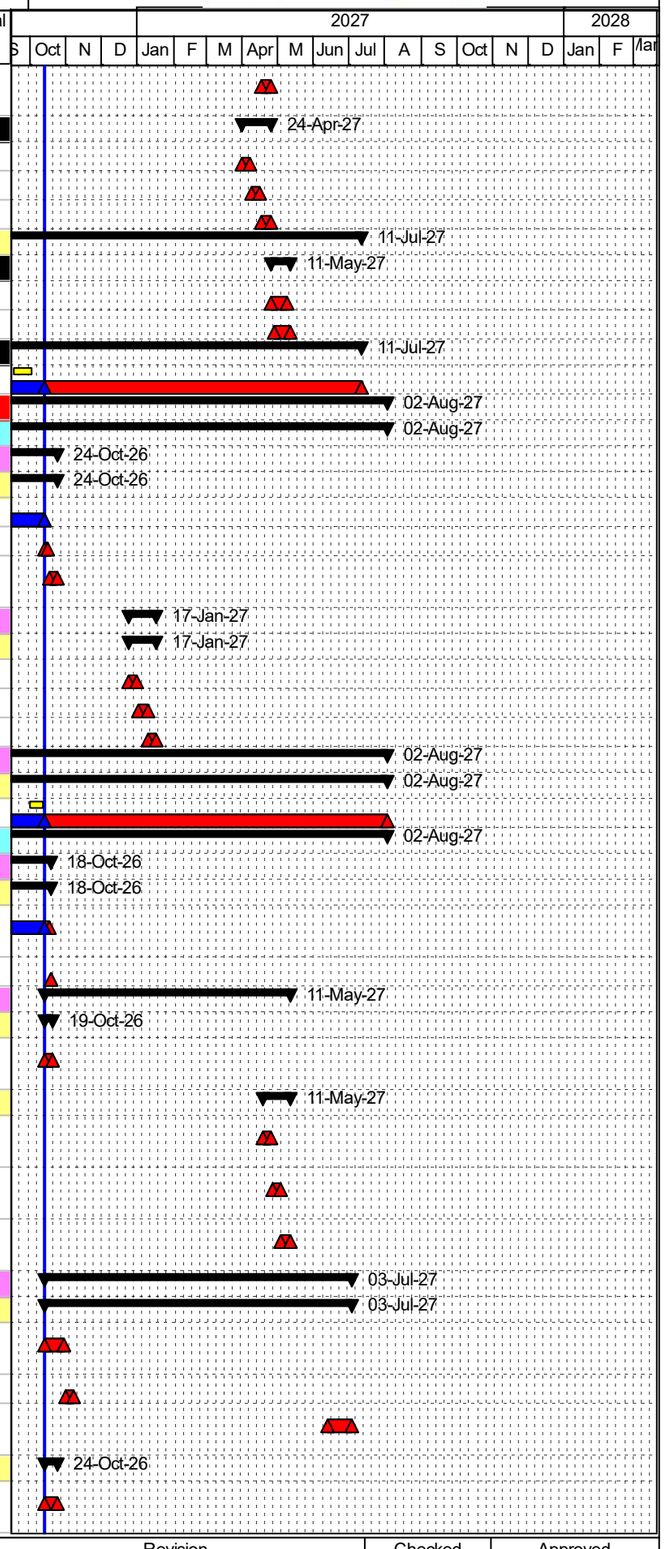

Primary Baseline | Actual Work | Summary
Remaining Work | Baseline Milestone
Critical Remaining Work | Milestone

Date	Revision	Checked	Approved
13-Oct-26	Third Industrial City		


Activity ID	Activity Name	Original Duration	Start	Finish	BL Project Start	BL Project Finish	Performance % Complete	Budgeted Total Cost	Remaining Total Cost
Distrubution Panel Boards		36	15-Apr-27	01-Jun-27	14-Jun-26	25-Jul-26	0%	18,011	18,011
CO-R11.S06-SL-17(	Foundation Excavation Works For Panel Boards of Street Lighting Network-[Road 11]-[SW-6]	12	15-Apr-27	28-Apr-27	14-Jun-26	27-Jun-26	0%	0	0
CO-R11.S06-SL-18(	Installation Works for Panel Board Concrete Foundations of Street Lighting Network-[Road 11]-[SW-6]	12	29-Apr-27	12-May-27	28-Jun-26	11-Jul-26	0%	0	0
CO-R11.S06-SL-19(	Installation Works for Lighting Panel Boards of Street Lighting Network-[Road 11]-[SW-6]	12	13-May-27	01-Jun-27	12-Jul-26	25-Jul-26	0%	0	0
CO-R11.S06-SL-22(	A wall of concrete blocks to install the KWH meter of Street Lighting Network-[Road 11]-[SW-6]	12	13-May-27	01-Jun-27	12-Jul-26	25-Jul-26	0%	18,011	18,011
Telecom Network		21	08-Apr-27	02-May-27	07-Jul-26	30-Jul-26	0%	9,401	9,401
Manholes Works		21	08-Apr-27	02-May-27	07-Jul-26	30-Jul-26	0%	9,401	9,401
CO-R11.S06-TE-1	Excavation Works for Manholes of Telecom Network-[Road 11]-[SW-6]	7	08-Apr-27	15-Apr-27	07-Jul-26	14-Jul-26	0%	1,257	1,257
CO-R11.S06-TE-1	Installation Works for Manholes of Telecom Network-[Road 11]-[SW-6]	7	17-Apr-27	24-Apr-27	15-Jul-26	22-Jul-26	0%	6,887	6,887
CO-R11.S06-TE-1	Backfilling Works for Manholes of Telecom Network-[Road 11]-[SW-6]	7	25-Apr-27	02-May-27	23-Jul-26	30-Jul-26	0%	1,257	1,257
Road Works		10	25-Aug-26 A	02-Aug-27	03-Oct-26	13-Oct-26	50%	62,462	62,462
Pavement Works		10	25-Aug-26 A	02-Aug-27	03-Oct-26	13-Oct-26	50%	62,462	62,462
CO-R11.S06-RD-F	Fixing of Interlock Tiles for Sidewalks Pavement-[Road 11]-[SW-6]	10	25-Aug-26 A	02-Aug-27	03-Oct-26	13-Oct-26	50%	62,462	62,462
Road 14 Local 1 (584 LM)		236	25-Aug-26 A	16-Aug-27	02-Aug-25	27-Oct-26	11.87%	778,646	778,646
SW_7		116	25-Aug-26 A	16-Aug-27	02-Aug-25	25-Oct-26	13.77%	335,519	335,519
Sewage Network		1	13-Oct-26	13-Oct-26	01-Sep-25	01-Sep-25	0%	6,319	6,319
Manholes		1	13-Oct-26	13-Oct-26	01-Sep-25	01-Sep-25	0%	6,319	6,319
CO-R14.S07-SW-	Testing Works for Main Line Manholes of Sewage Network-[Road 14]-[SW-7]	1	13-Oct-26	13-Oct-26	01-Sep-25	01-Sep-25	0%	6,319	6,319
Street Lighting Network		24	13-Oct-26	09-Nov-26	02-Aug-25	11-Jun-26	0%	9,399	9,399
Lighting Poles Works		18	13-Oct-26	02-Nov-26	18-May-26	11-Jun-26	0%	9,399	9,399
CO-R14.S07-SL-13(	Installation Works for Lighting Fixtures With Drop Wire of Street Lighting Network-[Road 14]-[SW-7]	18	13-Oct-26	02-Nov-26	18-May-26	11-Jun-26	0%	7,713	7,713
CO-R14.S07-SL-2	Testing Works for Lighting Poles of Street Lighting Network-[Road 14]-[SW-7]	5	13-Oct-26	18-Oct-26	07-Jun-26	11-Jun-26	0%	1,686	1,686
Distrubution Panel Boards		24	13-Oct-26	09-Nov-26	02-Aug-25	28-Aug-25	0%	0	0
CO-R14.S07-SL-17(	Foundation Excavation Works For Panel Boards of Street Lighting Network-[Road 14]-[SW-7]	18	13-Oct-26	02-Nov-26	02-Aug-25	21-Aug-25	0%	0	0
CO-R14.S07-SL-18(	Installation Works for Panel Board Concrete Foundations of Street Lighting Network-[Road 14]-[SW-7]	18	17-Oct-26	05-Nov-26	05-Aug-25	25-Aug-25	0%	0	0
CO-R14.S07-SL-22(	A wall of concrete blocks to install the KWH meter of Street Lighting Network-[Road 14]-[SW-7]	18	17-Oct-26	05-Nov-26	05-Aug-25	25-Aug-25	0%	0	0
CO-R14.S07-SL-19(	Installation Works for Lighting Panel Boards of Street Lighting Network-[Road 14]-[SW-7]	18	20-Oct-26	09-Nov-26	09-Aug-25	28-Aug-25	0%	0	0
Telecom Network		24	14-Jan-27	10-Feb-27	20-May-26	30-Jul-26	0%	69,527	69,527
Ducts Works		24	14-Jan-27	10-Feb-27	20-May-26	30-Jul-26	0%	56,984	56,984
CO-R14.S07-TE-10(	Trench Excavation and Bedding Works for Ducts of Telecom Network-[Road 14]-[SW-7]	3	14-Jan-27	17-Jan-27	20-May-26	23-May-26	0%	5,595	5,595
CO-R14.S07-TE-1	Pipes Laying Works for Ducts of Telecom Network-[Road 14]-[SW-7]	7	18-Jan-27	25-Jan-27	07-Jul-26	14-Jul-26	0%	34,304	34,304
CO-R14.S07-TE-1	Pouring Plain Concrete Above Ducts of Telecom Network-[Road 14]-[SW-7]	7	26-Jan-27	02-Feb-27	15-Jul-26	22-Jul-26	0%	5,595	5,595
CO-R14.S07-TE-13(	Trench Backfilling and Compaction Works for Ducts of Telecom Network-[Road 14]-[SW-7]	7	03-Feb-27	10-Feb-27	23-Jul-26	30-Jul-26	0%	11,491	11,491
Manholes Works		21	18-Jan-27	10-Feb-27	07-Jul-26	30-Jul-26	0%	12,543	12,543
CO-R14.S07-TE-1	Excavation Works for Manholes of Telecom Network-[Road 14]-[SW-7]	7	18-Jan-27	25-Jan-27	07-Jul-26	14-Jul-26	0%	1,885	1,885
CO-R14.S07-TE-1	Installation Works for Manholes of Telecom Network-[Road 14]-[SW-7]	7	26-Jan-27	02-Feb-27	15-Jul-26	22-Jul-26	0%	8,772	8,772
CO-R14.S07-TE-1	Backfilling Works for Manholes of Telecom Network-[Road 14]-[SW-7]	7	03-Feb-27	10-Feb-27	23-Jul-26	30-Jul-26	0%	1,885	1,885
Road Works		116	25-Aug-26 A	16-Aug-27	05-Sep-26	25-Oct-26	18.47%	250,274	250,274
Pre-Bituminous Construction		18	03-Feb-27	24-Feb-27	05-Sep-26	26-Sep-26	0%	157,847	157,847
CO-R14.S07-RD-I	Aggregate Base Course Layer for Road Works-[Road 14]-[SW-7]	18	03-Feb-27	24-Feb-27	05-Sep-26	26-Sep-26	0%	157,847	157,847
Pavement Works		12	25-Aug-26 A	16-Aug-27	12-Oct-26	25-Oct-26	50%	92,428	92,428
CO-R14.S07-RD-I	Fixing of Interlock Tiles for Sidewalks Pavement-[Road 14]-[SW-7]	12	25-Aug-26 A	16-Aug-27	12-Oct-26	25-Oct-26	50%	92,428	92,428
SW_8		235	25-Aug-26 A	16-Aug-27	15-Sep-25	27-Oct-26	10.43%	443,128	443,128
Sewage Network		1	13-Oct-26	13-Oct-26	15-Sep-25	15-Sep-25	0%	2,342	2,342

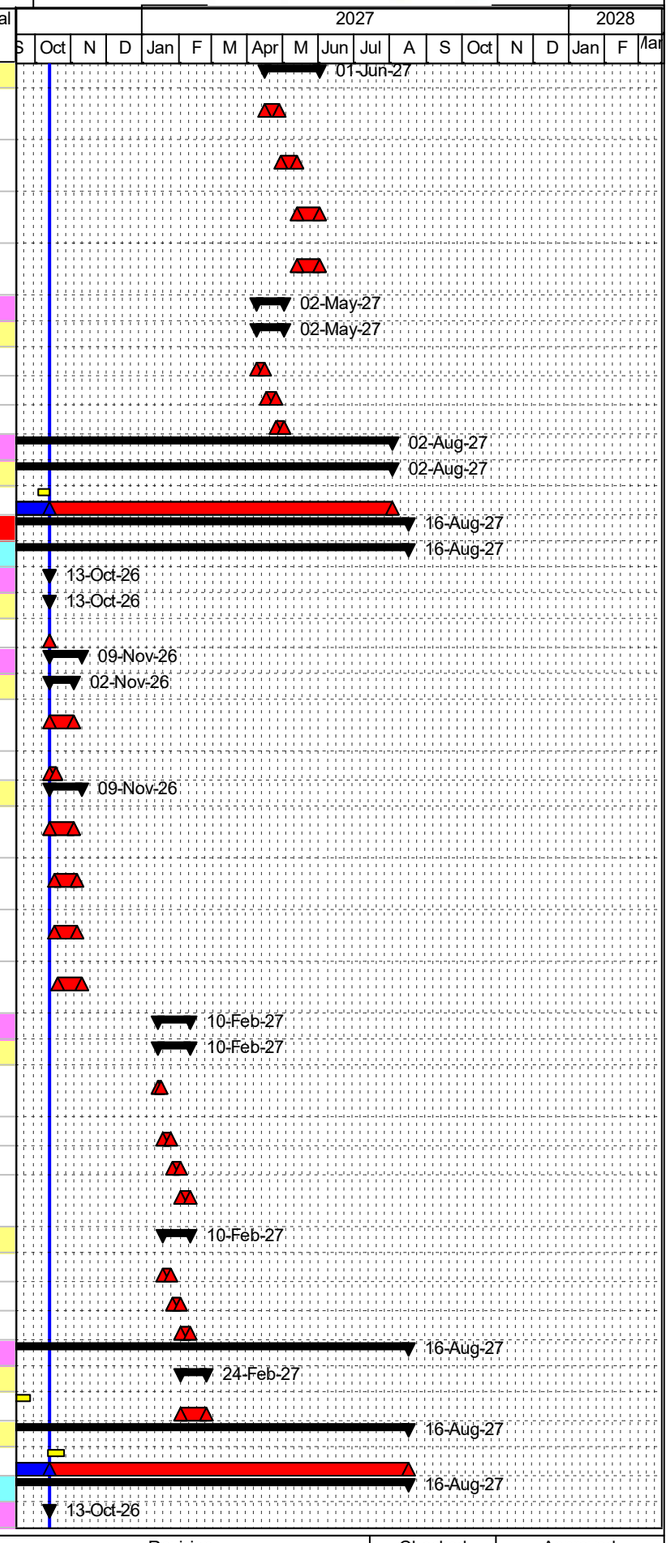

Primary Baseline
Remaining Work
Critical Remaining Work
Actual Work
Baseline Milestone
Milestone
Summary

Date	Revision	Checked	Approved
13-Oct-26	Third Industrial City		


Activity ID	Activity Name	Original Duration	Start	Finish	BL Project Start	BL Project Finish	Performance % Complete	Budgeted Total Cost	Remaining Total Cost
Manholes		1	13-Oct-26	13-Oct-26	15-Sep-25	15-Sep-25	0%	2,342	2,342
CO-R14.S08-SW-	Testing Works for Main Line Manholes of Sewage Network-[Road 14]-[SW-8]	1	13-Oct-26	13-Oct-26	15-Sep-25	15-Sep-25	0%	2,342	2,342
Potable Water Network		21	13-Oct-26	05-Nov-26	26-Feb-26	25-Mar-26	0%	53,020	53,020
Fire Hydrant		21	13-Oct-26	05-Nov-26	26-Feb-26	25-Mar-26	0%	53,020	53,020
CO-R14.S08-PW-14	Excavation Works for Fire Hydrants of Potable Water Network-[Road 14]-[SW-8]	7	13-Oct-26	20-Oct-26	26-Feb-26	05-Mar-26	0%	7,953	7,953
CO-R14.S08-PW-15	Installation Works for Fire Hydrant of Potable Water Network-[Road 14]-[SW-8]	7	21-Oct-26	28-Oct-26	07-Mar-26	14-Mar-26	0%	34,463	34,463
CO-R14.S08-PW-16	Trench Backfilling and Compaction Works for Fire Hydrants of Potable Water Network-[Road 14]-[SW-8]	7	29-Oct-26	05-Nov-26	15-Mar-26	25-Mar-26	0%	10,604	10,604
Street Lighting Network		235	13-Oct-26	24-Jul-27	24-Jun-26	15-Aug-26	0%	67,965	67,965
Lighting Poles Works		235	13-Oct-26	24-Jul-27	24-Jun-26	09-Aug-26	0%	41,146	41,146
CO-R14.S08-SL-2	Testing Works for Lighting Poles of Street Lighting Network-[Road 14]-[SW-8]	7	13-Oct-26	20-Oct-26	24-Jun-26	01-Jul-26	0%	15,989	15,989
CO-R14.S08-SL-85	Installation Works for Lighting Fixtures With Drop Wire of Street Lighting Network-[Road 14]-[SW-8]	18	04-Jul-27	24-Jul-27	20-Jul-26	09-Aug-26	0%	25,157	25,157
Distrubution Panel Boards		42	29-Apr-27	22-Jun-27	28-Jun-26	15-Aug-26	0%	26,818	26,818
CO-R14.S08-SL-DB	Foundation Excavation Works For Panel Boards of Street Lighting Network-[Road 14]-[SW-8]	18	29-Apr-27	25-May-27	28-Jun-26	18-Jul-26	0%	0	0
CO-R14.S08-SL-DB	Installation Works for Panel Board Concrete Foundations of Street Lighting Network-[Road 14]-[SW-8]	18	13-May-27	08-Jun-27	12-Jul-26	01-Aug-26	0%	0	0
CO-R14.S08-SL-22	A wall of concrete blocks to install the KWH meter of Street Lighting Network-[Road 14]-[SW-8]	25	13-May-27	16-Jun-27	12-Jul-26	09-Aug-26	0%	26,818	26,818
CO-R14.S08-SL-DB	Installation Works for Lighting Panel Boards of Street Lighting Network-[Road 14]-[SW-8]	18	02-Jun-27	22-Jun-27	26-Jul-26	15-Aug-26	0%	0	0
Telecom Network		93	18-Jan-27	10-May-27	07-Jun-26	08-Aug-26	0%	69,527	69,527
Ducts Works		24	18-Jan-27	14-Feb-27	07-Jun-26	08-Aug-26	0%	56,984	56,984
CO-R14.S08-TE-10	Trench Excavation and Bedding Works for Ducts of Telecom Network-[Road 14]-[SW-8]	3	18-Jan-27	20-Jan-27	07-Jun-26	09-Jun-26	0%	5,595	5,595
CO-R14.S08-TE-1	Pipes Laying Works for Ducts of Telecom Network-[Road 14]-[SW-8]	7	21-Jan-27	28-Jan-27	15-Jul-26	22-Jul-26	0%	34,304	34,304
CO-R14.S08-TE-1	Pouring Plain Concrete Above Ducts of Telecom Network-[Road 14]-[SW-8]	7	30-Jan-27	06-Feb-27	23-Jul-26	30-Jul-26	0%	5,595	5,595
CO-R14.S08-TE-13	Trench Backfilling and Compaction Works for Ducts of Telecom Network-[Road 14]-[SW-8]	7	07-Feb-27	14-Feb-27	01-Aug-26	08-Aug-26	0%	11,491	11,491
Manholes Works		21	17-Apr-27	10-May-27	15-Jul-26	08-Aug-26	0%	12,543	12,543
CO-R14.S08-TE-1	Excavation Works for Manholes of Telecom Network-[Road 14]-[SW-8]	7	17-Apr-27	24-Apr-27	15-Jul-26	22-Jul-26	0%	1,885	1,885
CO-R14.S08-TE-1	Installation Works for Manholes of Telecom Network-[Road 14]-[SW-8]	7	25-Apr-27	02-May-27	23-Jul-26	30-Jul-26	0%	8,772	8,772
CO-R14.S08-TE-1	Backfilling Works for Manholes of Telecom Network-[Road 14]-[SW-8]	7	03-May-27	10-May-27	01-Aug-26	08-Aug-26	0%	1,885	1,885
Road Works		194	25-Aug-26 A	16-Aug-27	02-Sep-26	27-Oct-26	18.47%	250,274	250,274
Pre-Bituminous Construction		18	12-May-27	07-Jun-27	02-Sep-26	22-Sep-26	0%	157,847	157,847
CO-R14.S08-RD-I	Aggregate Base Course Layer for Road Works-[Road 14]-[SW-8]	18	12-May-27	07-Jun-27	02-Sep-26	22-Sep-26	0%	157,847	157,847
Pavement Works		12	25-Aug-26 A	16-Aug-27	14-Oct-26	27-Oct-26	50%	92,428	92,428
CO-R14.S08-RD-I	Fixing of Interlock Tiles for Sidewalks Pavement-[Road 14]-[SW-8]	12	25-Aug-26 A	16-Aug-27	14-Oct-26	27-Oct-26	50%	92,428	92,428
Road 15 Local 1 (556 LM)		113	25-Aug-26 A	01-Sep-27	02-Jun-25	08-Nov-26	41.04%	180,060	180,060
SW_9		12	25-Aug-26 A	01-Sep-27	26-Oct-26	08-Nov-26	90%	52,781	52,781
Road Works		12	25-Aug-26 A	01-Sep-27	26-Oct-26	08-Nov-26	90%	52,781	52,781
Pavement Works		12	25-Aug-26 A	01-Sep-27	26-Oct-26	08-Nov-26	90%	52,781	52,781
CO-R15.S09-RD-I	Fixing of Interlock Tiles for Sidewalks Pavement-[Road 15]-[SW-9]	12	25-Aug-26 A	01-Sep-27	26-Oct-26	08-Nov-26	90%	52,781	52,781
SW_10		113	25-Aug-26 A	01-Sep-27	02-Jun-25	08-Nov-26	20.73%	127,279	127,279
Sewage Network		1	13-Oct-26	13-Oct-26	05-Jul-25	06-Jul-25	0%	2,883	2,883
Manholes		1	13-Oct-26	13-Oct-26	05-Jul-25	06-Jul-25	0%	2,883	2,883
CO-R15.S10-SW-21	Testing Works for Main Line Manholes of Sewage Network-[Road 15]-[SW-10]	1	13-Oct-26	13-Oct-26	05-Jul-25	06-Jul-25	0%	2,883	2,883
Street Lighting Network		113	13-Oct-26	21-Feb-27	02-Jun-25	02-Feb-26	0%	41,317	41,317
Lighting Poles Works		113	13-Oct-26	21-Feb-27	13-Jan-26	02-Feb-26	0%	24,492	24,492
CO-R15.S10-SL-20	Testing Works for Lighting Poles of Street Lighting Network-[Road 15]-[SW-10]	5	13-Oct-26	18-Oct-26	27-Jan-26	02-Feb-26	0%	9,517	9,517

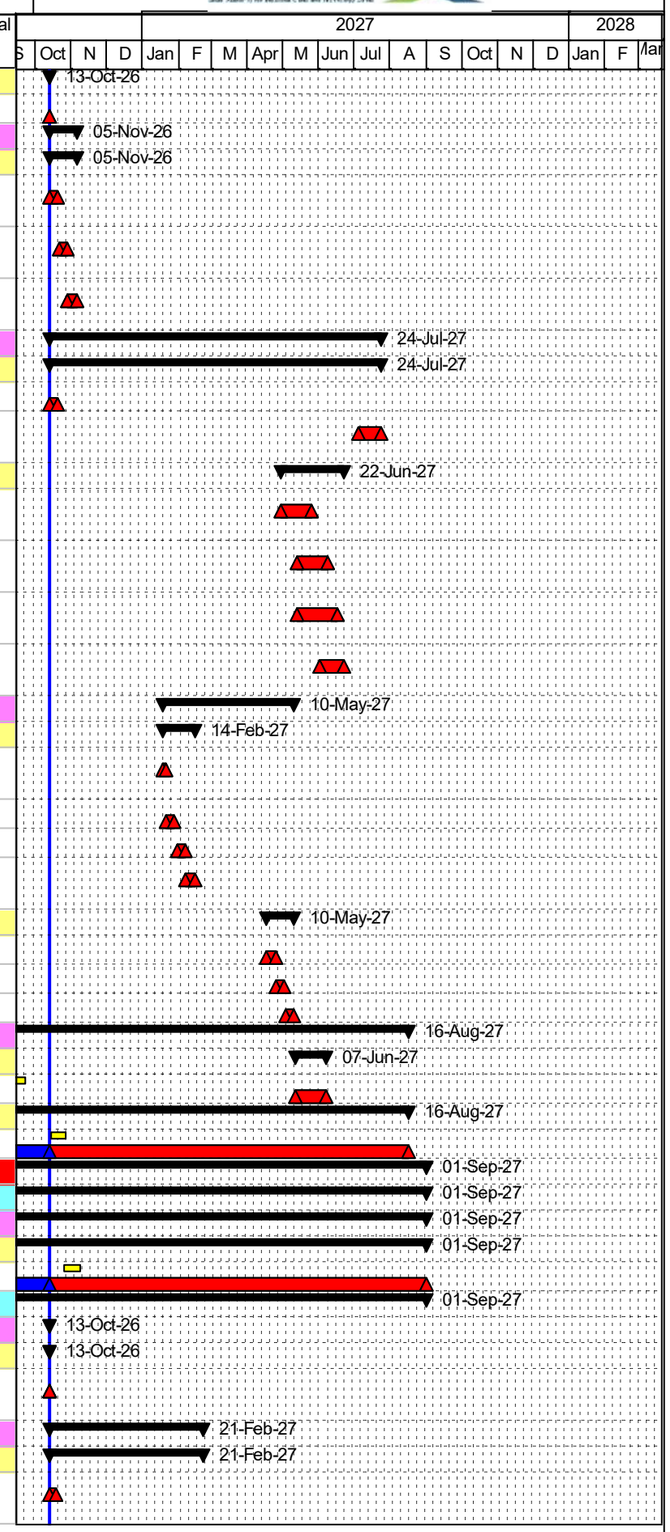

Primary Baseline
Remaining Work
Critical Remaining Work
Actual Work
Baseline Milestone
Milestone
Summary

Date	Revision	Checked	Approved
13-Oct-26	Third Industrial City		


Activity ID	Activity Name	Original Duration	Start	Finish	BL Project Start	BL Project Finish	Performance % Complete	Budgeted Total Cost	Remaining Total Cost
CO-R15.S10-SL-13(	Installation Works for Lighting Fixtures With Drop Wire of Street Lighting Network-[Road 15]-[SW-10]	18	01-Feb-27	21-Feb-27	13-Jan-26	02-Feb-26	0%	14,975	14,975
Distrubution Panel Boards		24	13-Oct-26	09-Nov-26	02-Jun-25	03-Jul-25	0%	16,825	16,825
CO-R15.S10-SL-17(	Foundation Excavation Works For Panel Boards of Street Lighting Network-[Road 15]-[SW-10]	18	13-Oct-26	02-Nov-26	02-Jun-25	26-Jun-25	0%	0	0
CO-R15.S10-SL-18(	Installation Works for Panel Board Concrete Foundations of Street Lighting Network-[Road 15]-[SW-10]	18	17-Oct-26	05-Nov-26	10-Jun-25	30-Jun-25	0%	0	0
CO-R15.S10-SL-22(	A wall of concrete blocks to install the KWH meter of Street Lighting Network-[Road 15]-[SW-10]	18	17-Oct-26	05-Nov-26	10-Jun-25	30-Jun-25	0%	16,825	16,825
CO-R15.S10-SL-19(	Installation Works for Lighting Panel Boards of Street Lighting Network-[Road 15]-[SW-10]	18	20-Oct-26	09-Nov-26	14-Jun-25	03-Jul-25	0%	0	0
Potable Water Network		18	14-Oct-26	03-Nov-26	08-Mar-26	31-Mar-26	0%	30,297	30,297
Fire Hydrant		18	14-Oct-26	03-Nov-26	08-Mar-26	31-Mar-26	0%	30,297	30,297
CO-R15.S10-PW-14	Excavation Works for Fire Hydrants of Potable Water Network-[Road 15]-[SW-10]	6	14-Oct-26	20-Oct-26	08-Mar-26	14-Mar-26	0%	4,545	4,545
CO-R15.S10-PW-15	Installation Works for Fire Hydrant of Potable Water Network-[Road 15]-[SW-10]	6	21-Oct-26	27-Oct-26	15-Mar-26	24-Mar-26	0%	19,693	19,693
CO-R15.S10-PW-16	Trench Backfilling and Compaction Works for Fire Hydrants of Potable Water Network-[Road 15]-[SW-10]	6	28-Oct-26	03-Nov-26	25-Mar-26	31-Mar-26	0%	6,059	6,059
Road Works		10	25-Aug-26 A	01-Sep-27	28-Oct-26	08-Nov-26	50%	52,781	52,781
Pavement Works		10	25-Aug-26 A	01-Sep-27	28-Oct-26	08-Nov-26	50%	52,781	52,781
CO-R15.S10-RD-I	Fixing of Interlock Tiles for Sidewalks Pavement-[Road 15]-[SW-10]	10	25-Aug-26 A	01-Sep-27	28-Oct-26	08-Nov-26	50%	52,781	52,781
Road 16 Local 1 (527 LM)		33	25-Aug-26 A	15-Sep-27	29-Mar-26	19-Nov-26	69.19%	131,033	131,033
SW_11		10	25-Aug-26 A	15-Sep-27	05-Nov-26	16-Nov-26	90%	50,368	50,368
Road Works		10	25-Aug-26 A	15-Sep-27	05-Nov-26	16-Nov-26	90%	50,368	50,368
Pavement Works		10	25-Aug-26 A	15-Sep-27	05-Nov-26	16-Nov-26	90%	50,368	50,368
CO-R16.S11-RD-I	Fixing of Interlock Tiles for Sidewalks Pavement-[Road 16]-[SW-11]	10	25-Aug-26 A	15-Sep-27	05-Nov-26	16-Nov-26	90%	50,368	50,368
SW_12		33	25-Aug-26 A	15-Sep-27	29-Mar-26	19-Nov-26	56.2%	80,665	80,665
Potable Water Network		25	13-Oct-26	10-Nov-26	29-Mar-26	18-Apr-26	0%	30,297	30,297
Fire Hydrant		25	13-Oct-26	10-Nov-26	29-Mar-26	18-Apr-26	0%	30,297	30,297
CO-R16.S12-PW-14	Excavation Works for Fire Hydrants of Potable Water Network-[Road 16]-[SW-12]	6	13-Oct-26	19-Oct-26	29-Mar-26	04-Apr-26	0%	4,545	4,545
CO-R16.S12-PW-15	Installation Works for Fire Hydrant of Potable Water Network-[Road 16]-[SW-12]	6	28-Oct-26	03-Nov-26	05-Apr-26	11-Apr-26	0%	19,693	19,693
CO-R16.S12-PW-16	Trench Backfilling and Compaction Works for Fire Hydrants of Potable Water Network-[Road 16]-[SW-12]	6	04-Nov-26	10-Nov-26	12-Apr-26	18-Apr-26	0%	6,059	6,059
Road Works		10	25-Aug-26 A	15-Sep-27	09-Nov-26	19-Nov-26	90%	50,368	50,368
Pavement Works		10	25-Aug-26 A	15-Sep-27	09-Nov-26	19-Nov-26	90%	50,368	50,368
CO-R16.S12-RD-I	Fixing of Interlock Tiles for Sidewalks Pavement-[Road 16]-[SW-12]	10	25-Aug-26 A	15-Sep-27	09-Nov-26	19-Nov-26	90%	50,368	50,368
Road 17 Local 1 (500 LM)		61	13-Oct-26	22-Dec-26	16-Apr-25	01-Sep-26	0%	102,158	102,158
SW_14		61	13-Oct-26	22-Dec-26	16-Apr-25	01-Sep-26	0%	102,158	102,158
Sewage Network		1	13-Oct-26	13-Oct-26	21-May-25	21-May-25	0%	1,518	1,518
Manholes		1	13-Oct-26	13-Oct-26	21-May-25	21-May-25	0%	1,518	1,518
CO-R17.S14-SW-21	Testing Works for Main Line Manholes of Sewage Network-[Road 17]-[SW-14]	1	13-Oct-26	13-Oct-26	21-May-25	21-May-25	0%	1,518	1,518
Street Lighting Network		61	13-Oct-26	22-Dec-26	16-Apr-25	14-Dec-25	0%	71,659	71,659
Lighting Poles Works		61	13-Oct-26	22-Dec-26	24-Nov-25	14-Dec-25	0%	44,085	44,085
CO-R17.S14-SL-20(	Testing Works for Lighting Poles of Street Lighting Network-[Road 17]-[SW-14]	5	13-Oct-26	18-Oct-26	08-Dec-25	14-Dec-25	0%	17,131	17,131
CO-R17.S14-SL-13(	Installation Works for Lighting Fixtures With Drop Wire of Street Lighting Network-[Road 17]-[SW-14]	18	02-Dec-26	22-Dec-26	24-Nov-25	14-Dec-25	0%	26,954	26,954
Distrubution Panel Boards		24	13-Oct-26	09-Nov-26	16-Apr-25	13-May-25	0%	27,573	27,573
CO-R17.S14-SL-17(	Foundation Excavation Works For Panel Boards of Street Lighting Network-[Road 17]-[SW-14]	18	13-Oct-26	02-Nov-26	16-Apr-25	06-May-25	0%	0	0
CO-R17.S14-SL-18(	Installation Works for Panel Board Concrete Foundations of Street Lighting Network-[Road 17]-[SW-14]	18	17-Oct-26	05-Nov-26	20-Apr-25	10-May-25	0%	0	0

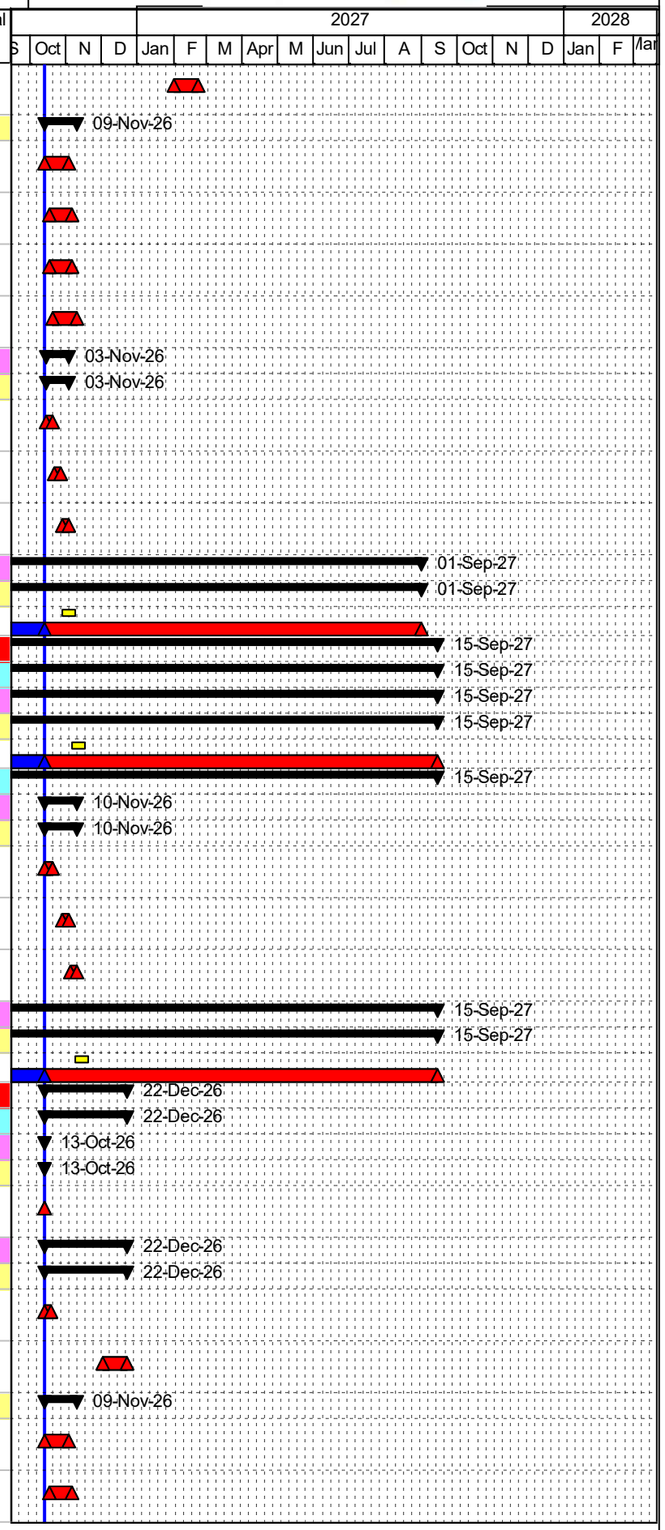

Primary Baseline · Actual Work · Summary
Remaining Work · Baseline Milestone
Critical Remaining Work · Milestone

Date	Revision	Checked	Approved
13-Oct-26	Third Industrial City		


Activity ID	Activity Name	Original Duration	Start	Finish	BL Project Start	BL Project Finish	Performance % Complete	Budgeted Total Cost	Remaining Total Cost
CO-R17.S14-SL-22(	A wall of concrete blocks to install the KWH meter of Street Lighting Network-[Road 17]-[SW-14]	18	17-Oct-26	05-Nov-26	20-Apr-25	10-May-25	0%	27,573	27,573
CO-R17.S14-SL-19(	Installation Works for Lighting Panel Boards of Street Lighting Network-[Road 17]-[SW-14]	18	20-Oct-26	09-Nov-26	23-Apr-25	13-May-25	0%	0	0
Potable Water Network		30	14-Oct-26	17-Nov-26	21-Apr-26	11-May-26	0%	22,723	22,723
Fire Hydrant		30	14-Oct-26	17-Nov-26	21-Apr-26	11-May-26	0%	22,723	22,723
CO-R17.S14-PW-14	Excavation Works for Fire Hydrants of Potable Water Network-[Road 17]-[SW-14]	6	14-Oct-26	20-Oct-26	21-Apr-26	27-Apr-26	0%	3,408	3,408
CO-R17.S14-PW-15	Installation Works for Fire Hydrant of Potable Water Network-[Road 17]-[SW-14]	6	04-Nov-26	10-Nov-26	28-Apr-26	04-May-26	0%	14,770	14,770
CO-R17.S14-PW-16	Trench Backfilling and Compaction Works for Fire Hydrants of Potable Water Network-[Road 17]-[SW-14]	6	11-Nov-26	17-Nov-26	05-May-26	11-May-26	0%	4,545	4,545
Telecom Network		21	13-Oct-26	05-Nov-26	09-Aug-26	01-Sep-26	0%	6,258	6,258
Manholes Works		21	13-Oct-26	05-Nov-26	09-Aug-26	01-Sep-26	0%	6,258	6,258
CO-R17.S14-TE-1	Excavation Works for Manholes of Telecom Network-[Road 17]-[SW-14]	7	13-Oct-26	20-Oct-26	09-Aug-26	16-Aug-26	0%	628	628
CO-R17.S14-TE-1	Installation Works for Manholes of Telecom Network-[Road 17]-[SW-14]	7	21-Oct-26	28-Oct-26	17-Aug-26	24-Aug-26	0%	5,002	5,002
CO-R17.S14-TE-1	Backfilling Works for Manholes of Telecom Network-[Road 17]-[SW-14]	7	29-Oct-26	05-Nov-26	25-Aug-26	01-Sep-26	0%	628	628
Road 18 Local 1 (479 LM)		35	13-Oct-26	22-Nov-26	19-Mar-25	27-Nov-25	0%	51,658	51,658
SW_16		35	13-Oct-26	22-Nov-26	19-Mar-25	27-Nov-25	0%	51,658	51,658
Street Lighting Network		35	13-Oct-26	22-Nov-26	19-Mar-25	27-Nov-25	0%	36,510	36,510
Lighting Poles Works		35	13-Oct-26	22-Nov-26	08-Nov-25	27-Nov-25	0%	20,573	20,573
CO-R18.S16-SL-20(	Testing Works for Lighting Poles of Street Lighting Network-[Road 18]-[SW-16]	5	13-Oct-26	18-Oct-26	22-Nov-25	27-Nov-25	0%	7,995	7,995
CO-R18.S16-SL-13(	Installation Works for Lighting Fixtures With Drop Wire of Street Lighting Network-[Road 18]-[SW-16]	18	02-Nov-26	22-Nov-26	08-Nov-25	27-Nov-25	0%	12,579	12,579
Distrubution Panel Boards		24	13-Oct-26	09-Nov-26	19-Mar-25	20-Apr-25	0%	15,936	15,936
CO-R18.S16-SL-17(	Foundation Excavation Works For Panel Boards of Street Lighting Network-[Road 18]-[SW-16]	18	13-Oct-26	02-Nov-26	19-Mar-25	13-Apr-25	0%	0	0
CO-R18.S16-SL-18(	Installation Works for Panel Board Concrete Foundations of Street Lighting Network-[Road 18]-[SW-16]	18	17-Oct-26	05-Nov-26	23-Mar-25	16-Apr-25	0%	0	0
CO-R18.S16-SL-22(	A wall of concrete blocks to install the KWH meter of Street Lighting Network-[Road 18]-[SW-16]	18	17-Oct-26	05-Nov-26	23-Mar-25	16-Apr-25	0%	15,936	15,936
CO-R18.S16-SL-19(	Installation Works for Lighting Panel Boards of Street Lighting Network-[Road 18]-[SW-16]	18	20-Oct-26	09-Nov-26	26-Mar-25	20-Apr-25	0%	0	0
Potable Water Network		18	13-Oct-26	02-Nov-26	23-Aug-25	11-Sep-25	0%	15,149	15,149
Fire Hydrant		18	13-Oct-26	02-Nov-26	23-Aug-25	11-Sep-25	0%	15,149	15,149
CO-R18.S16-PW-25	Excavation Works for Fire Hydrants of Potable Water Network-[Road 18]-[SW-16]	6	13-Oct-26	19-Oct-26	23-Aug-25	28-Aug-25	0%	2,272	2,272
CO-R18.S16-PW-26	Installation Works for Fire Hydrant of Potable Water Network-[Road 18]-[SW-16]	6	20-Oct-26	26-Oct-26	30-Aug-25	04-Sep-25	0%	9,847	9,847
CO-R18.S16-PW-27	Trench Backfilling and Compaction Works for Fire Hydrants of Potable Water Network-[Road 18]-[SW-16]	6	27-Oct-26	02-Nov-26	06-Sep-25	11-Sep-25	0%	3,030	3,030
Finishes for Infrastructure Networks		426	01-Jun-26 A	06-Dec-27	04-May-26	28-Dec-26	15.53%	9,396,573	9,294,616
Phase 2 Block "J"		426	01-Jun-26 A	06-Dec-27	04-May-26	28-Dec-26	15.53%	9,396,573	9,294,616
Road 09 Local 2 (2278 LM)		404	01-Jun-26 A	10-Nov-27	02-Jun-26	30-Nov-26	23.1%	3,449,609	3,347,652
Sewage Network		286	01-Jun-26 A	28-Jun-27	19-Jul-26	18-Aug-26	68.42%	289,897	289,897
Testing and Finishes		286	01-Jun-26 A	28-Jun-27	19-Jul-26	18-Aug-26	68.42%	289,897	289,897
CO-R09-SW-TF-1(	Final Testing For Main Line of Sewage Network-[Road 09]	12	01-Jun-26 A	10-Jun-27	19-Jul-26	01-Aug-26	95%	208,794	208,794
CO-R09-SW-TF-110	Install Manhole Cover Works for External Finishes of Sewage Network-[Road 09]	12	12-Jun-27	24-Jun-27	02-Aug-26	15-Aug-26	0%	40,552	40,552
CO-R09-SW-TF-120	Main Manhole Internal Finishes (Benching + Insulation) of Sewage Network-[Road 09]	12	15-Jun-27	28-Jun-27	05-Aug-26	18-Aug-26	0%	40,552	40,552
Storm Drainage Network		43	17-Jun-26 A	29-Jun-27	15-Jul-26	02-Sep-26	78.91%	758,679	656,721
Testing and Finishes		43	17-Jun-26 A	29-Jun-27	15-Jul-26	02-Sep-26	78.91%	758,679	656,721
CO-R09-SD-TF-1(	Testing Work for Pipes of Storm Drainage Network-[Road 09]	12	17-Jun-26 A	12-Jun-27	19-Jul-26	01-Aug-26	75%	101,957	0

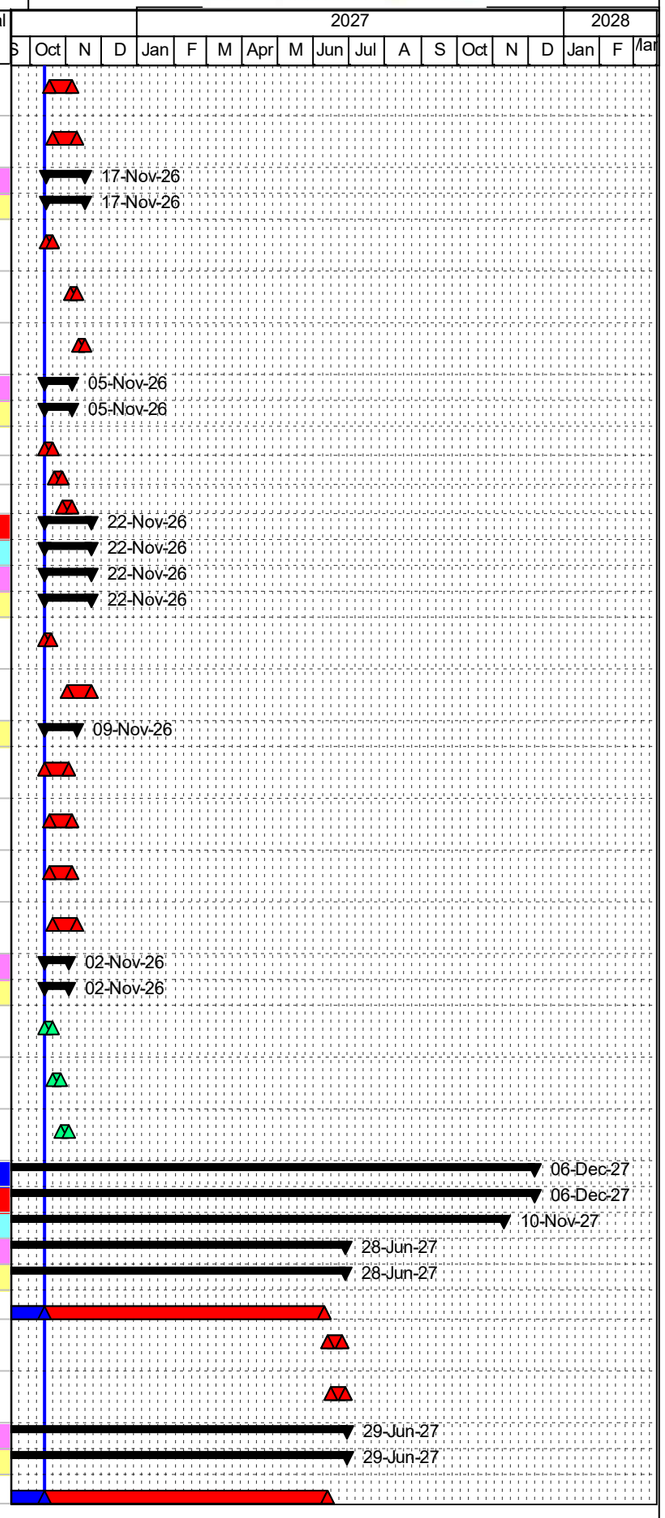

Primary Baseline
Remaining Work
Critical Remaining Work
Actual Work
Baseline Milestone
Milestone
Summary

Date	Revision	Checked	Approved
13-Oct-26	Third Industrial City		


Activity ID	Activity Name	Original Duration	Start	Finish	BL Project Start	BL Project Finish	Performance % Complete	Budgeted Total Cost	Remaining Total Cost
CO-R09-SD-TF-110	Install Catch Basin Cover Works for External Finishes of Storm Drainage Network-[Road 09]	16	20-Jun-26 A	01-Apr-27	15-Jul-26	02-Aug-26	20%	27,719	27,719
CO-R09-SD-TF-120	Main Manhole Internal Finishes (Benching + Insulation) for Storm Drainage Network-[Road 09]	16	21-Jun-26 A	29-Jun-27	16-Aug-26	02-Sep-26	85%	601,283	601,283
CO-R09-SD-TF-130	Catch Basin Internal Finishes (Benching + Insulation) for Storm Drainage Network-[Road 09]	16	22-Jun-26 A	29-Jun-27	16-Aug-26	02-Sep-26	20%	27,719	27,719
Potable Water Network		33	17-Jun-27	25-Jul-27	02-Aug-26	08-Sep-26	0%	39,232	39,232
Testing and Finishes		33	17-Jun-27	25-Jul-27	02-Aug-26	08-Sep-26	0%	39,232	39,232
CO-R09-PW-TF-1(	Testing Work for Main Line of Potable Water Network-[Road 09]	9	17-Jun-27	27-Jun-27	02-Aug-26	11-Aug-26	0%	39,232	39,232
CO-R09-PW-TF-100	Final Finishes works and Covers for Valves and Valve Chambers of Potable Water Network-[Road 09]	12	28-Jun-27	11-Jul-27	12-Aug-26	25-Aug-26	0%	0	0
CO-R09-PW-TF-120	Fire Hydrant Finishies (S.Box + Safety + Marker Post) of Potable Water Network-[Road 09]	12	12-Jul-27	25-Jul-27	26-Aug-26	08-Sep-26	0%	0	0
Irrigation Network		16	08-Jun-27	26-Jun-27	29-Jul-26	16-Aug-26	0%	21,307	21,307
Testing and Finishes		16	08-Jun-27	26-Jun-27	29-Jul-26	16-Aug-26	0%	21,307	21,307
CO-R09-IR-TF-10(	Final Testing (pressure tests) of Irrigation Network-[Road 09]	16	08-Jun-27	26-Jun-27	29-Jul-26	16-Aug-26	0%	21,307	21,307
Street Lighting Network		86	03-Jun-27	11-Sep-27	02-Jun-26	09-Sep-26	0%	189,757	189,757
Termination and Testing Works		84	03-Jun-27	08-Sep-27	02-Jun-26	07-Sep-26	0%	177,971	177,971
CO-R09-SL-TF-100	Termination Works For Lighting Poles Cables of Street Lighting Network-[Road 09]	12	03-Jun-27	16-Jun-27	02-Jun-26	15-Jun-26	0%	80,959	80,959
CO-R09-SL-TF-110	Termination Works For Panel Board Cables of Street Lighting Network-[Road 09]	11	16-Aug-27	28-Aug-27	15-Aug-26	26-Aug-26	0%	64,675	64,675
CO-R09-SL-TF-38	Testing Works For Panel Board Cables of Street Lighting Network-[Road 09]	10	28-Aug-27	08-Sep-27	26-Aug-26	07-Sep-26	0%	32,337	32,337
Earthing System Works		74	17-Jun-27	11-Sep-27	16-Jun-26	09-Sep-26	0%	11,785	11,785
CO-R09-SL-ES-100	Install Earthing System Works for Lighting Poles of Street Lighting Network-[Road 09]	12	17-Jun-27	30-Jun-27	16-Jun-26	29-Jun-26	0%	6,125	6,125
CO-R09-SL-ES-110	Install Earthing System Works for Lighting Panel Boards of Street Lighting Network-[Road 09]	12	28-Aug-27	11-Sep-27	26-Aug-26	09-Sep-26	0%	5,660	5,660
Medium Voltage Network		16	10-Feb-27	01-Mar-27	21-Jun-26	08-Jul-26	0%	0	0
Termination and Testing Works		16	10-Feb-27	01-Mar-27	21-Jun-26	08-Jul-26	0%	0	0
CO-R09-MV-TF-10	Termination Works of Medium Voltage Network-[Road 09]	16	10-Feb-27	01-Mar-27	21-Jun-26	08-Jul-26	0%	0	0
Road Works		51	11-Sep-27	10-Nov-27	24-Sep-26	30-Nov-26	0%	2,150,738	2,150,738
Bituminous Construction		21	11-Sep-27	06-Oct-27	24-Sep-26	26-Oct-26	0%	2,058,508	2,058,508
CO-R09-S1-RD-F-	Application of Prime Coat Layer for Road Works - S.W 01-[Road 09]	12	11-Sep-27	26-Sep-27	24-Sep-26	08-Oct-26	0%	576,152	576,152
CO-R09-S2-RD-F-	Application of Prime Coat Layer for Road Works- S.W 02-[Road 09]	18	11-Sep-27	03-Oct-27	01-Oct-26	22-Oct-26	0%	576,152	576,152
CO-R09-S1-RD-F-1	Bituminous Base & Wearing Courses Layers for Road Works- S.W 01-[Road 09]	12	14-Sep-27	29-Sep-27	28-Sep-26	12-Oct-26	0%	453,102	453,102
CO-R09-S2-RD-F-1	Bituminous Base & Wearing Courses Layers for Road Works- S.W 02-[Road 09]	18	14-Sep-27	06-Oct-27	05-Oct-26	26-Oct-26	0%	453,102	453,102
Traffic Signs Boards and Roads Marking		36	29-Sep-27	10-Nov-27	12-Oct-26	30-Nov-26	0%	92,229	92,229
CO-R09-S1-RD-F-	Application of Road Marking Works For Road Works- S.W 01-[Road 09]	12	29-Sep-27	13-Oct-27	12-Oct-26	26-Oct-26	0%	33,593	33,593
CO-R09-S2-RD-F-	Application of Road Marking Works For Road Works- S.W 02-[Road 09]	15	06-Oct-27	24-Oct-27	26-Oct-26	12-Nov-26	0%	33,593	33,593
CO-R09-S1-RD-F-	Installation Works of Traffic Signs Boards For Road Works- S.W 01-[Road 09]	12	13-Oct-27	27-Oct-27	26-Oct-26	09-Nov-26	0%	12,522	12,522
CO-R09-S2-RD-F-	Installation Works of Traffic Signs Boards For Road Works- S.W 02-[Road 09]	15	24-Oct-27	10-Nov-27	12-Nov-26	30-Nov-26	0%	12,522	12,522
Road 10 Local 2 (2352 LM)		308	17-Jun-26 A	09-Aug-27	04-May-26	31-Oct-26	12.79%	3,459,716	3,459,716
Sewage Network		27	28-Apr-27	03-Jun-27	29-Jul-26	29-Aug-26	0%	153,798	153,798
Testing and Finishes		27	28-Apr-27	03-Jun-27	29-Jul-26	29-Aug-26	0%	153,798	153,798
CO-R10-SW-TF-1(	Final Testing For Main Line of Sewage Network-[Road 10]	12	28-Apr-27	11-May-27	29-Jul-26	11-Aug-26	0%	115,643	115,643
CO-R10-SW-TF-110	Install Manhole Cover Works for External Finishes of Sewage Network-[Road 10]	12	12-May-27	31-May-27	12-Aug-26	25-Aug-26	0%	19,078	19,078
CO-R10-SW-TF-130	Main Manhole Internal Finishes (Benching + Insulation) of Sewage Network-[Road 10]	12	22-May-27	03-Jun-27	16-Aug-26	29-Aug-26	0%	19,078	19,078
Storm Drainage Network		35	17-Jun-26 A	31-May-27	04-Aug-26	13-Sep-26	79.27%	558,233	558,233
Testing and Finishes		35	17-Jun-26 A	31-May-27	04-Aug-26	13-Sep-26	79.27%	558,233	558,233

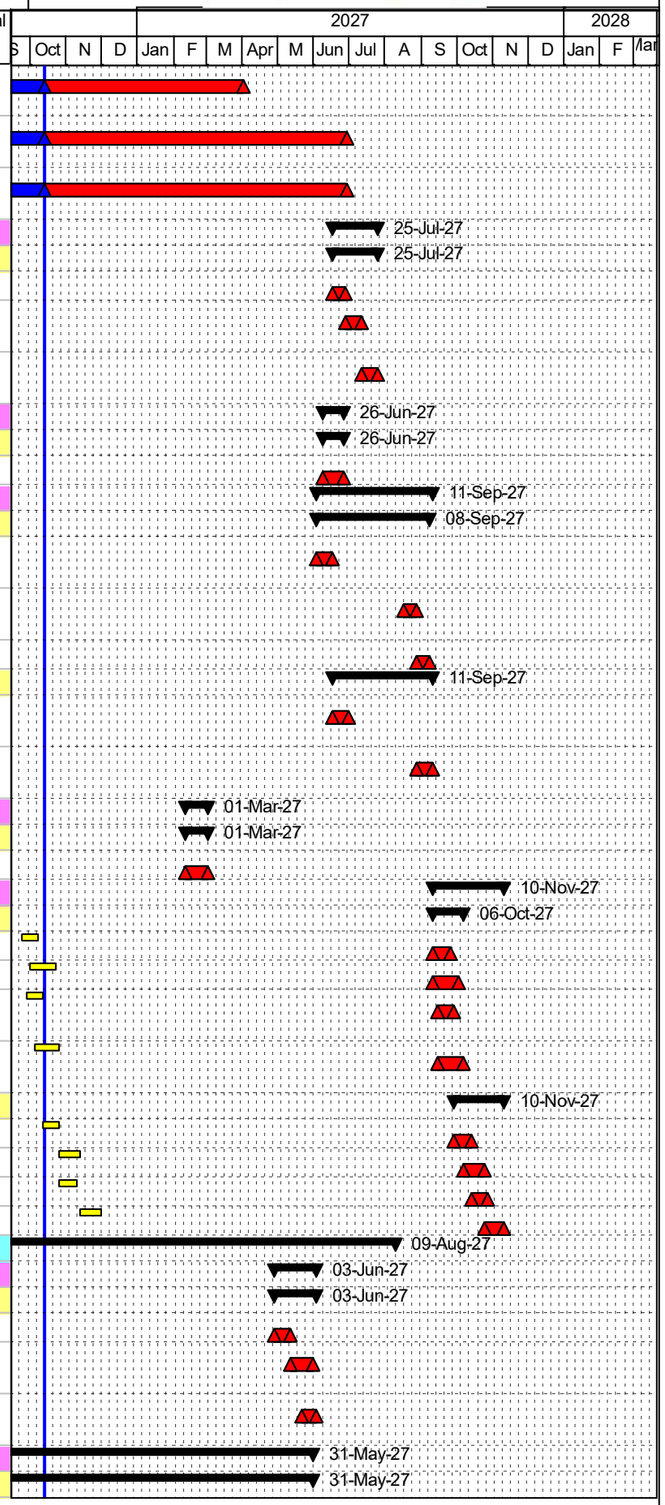

Primary Baseline · Actual Work · Summary
Remaining Work · Baseline Milestone
Critical Remaining Work · Milestone

Date	Revision	Checked	Approved
13-Oct-26	Third Industrial City		


Activity ID	Activity Name	Original Duration	Start	Finish	BL Project Start	BL Project Finish	Performance % Complete	Budgeted Total Cost	Remaining Total Cost
CO-R10-SD-TF-110	Install Catch Basin Cover Works for External Finishes of Storm Drainage Network-[Road 10]	16	17-Jun-26 A	11-May-27	04-Aug-26	22-Aug-26	20%	27,796	27,796
CO-R10-SD-TF-120	Main Manhole Internal Finishes (Benching + Insulation) for Storm Drainage Network-[Road 10]	12	18-Jun-26 A	31-May-27	26-Aug-26	08-Sep-26	85%	502,642	502,642
CO-R10-SD-TF-130	Catch Basin Internal Finishes (Benching + Insulation) for Storm Drainage Network-[Road 10]	16	22-Jun-26 A	31-May-27	26-Aug-26	13-Sep-26	35%	27,795	27,795
Potable Water Network		97	15-Mar-27	11-Jul-27	08-Aug-26	03-Sep-26	0%	299,945	299,945
Testing and Finishes		97	15-Mar-27	11-Jul-27	08-Aug-26	03-Sep-26	0%	299,945	299,945
CO-R10-PW-TF-100	Final Finishes works and Covers for Valves and Valve Chambers of Potable Water Network-[Road 10]	12	15-Mar-27	28-Mar-27	08-Aug-26	20-Aug-26	0%	0	0
CO-R10-PW-TF-120	Fire Hydrant Finishies (S.Box + Safety + Marker Post) of Potable Water Network-[Road 10]	12	29-Mar-27	11-Apr-27	22-Aug-26	03-Sep-26	0%	0	0
CO-R10-PW-TF-1(	Testing Work for Main Line of Potable Water Network-[Road 10]	12	28-Jun-27	11-Jul-27	12-Aug-26	25-Aug-26	0%	299,945	299,945
Irrigation Network		10	09-May-27	25-May-27	09-Aug-26	19-Aug-26	0%	100,763	100,763
Testing and Finishes		10	09-May-27	25-May-27	09-Aug-26	19-Aug-26	0%	100,763	100,763
CO-R10-IR-TF-12(	Final Testing (pressure tests) of Irrigation Network-[Road 10]	10	09-May-27	25-May-27	09-Aug-26	19-Aug-26	0%	100,763	100,763
Street Lighting Network		62	15-Mar-27	31-May-27	04-May-26	23-Jul-26	0%	190,052	190,052
Termination and Testing Works		62	15-Mar-27	31-May-27	04-May-26	23-Jul-26	0%	178,267	178,267
CO-R10-SL-TF-140	Termination Works For Lighting Poles Cables of Street Lighting Network-[Road 10]	12	15-Mar-27	28-Mar-27	04-May-26	17-May-26	0%	81,254	81,254
CO-R10-SL-TF-150	Termination Works For Panel Board Cables of Street Lighting Network-[Road 10]	12	10-May-27	29-May-27	08-Jul-26	21-Jul-26	0%	64,675	64,675
CO-R10-SL-TF-38	Testing Works For Panel Board Cables of Street Lighting Network-[Road 10]	2	30-May-27	31-May-27	22-Jul-26	23-Jul-26	0%	32,337	32,337
Earthing System Works		27	29-Mar-27	28-Apr-27	18-May-26	22-Jun-26	0%	11,785	11,785
CO-R10-SL-ES-140	Install Earthing System Works for Lighting Poles of Street Lighting Network-[Road 10]	12	29-Mar-27	11-Apr-27	18-May-26	04-Jun-26	0%	6,125	6,125
CO-R10-SL-ES-150	Install Earthing System Works for Lighting Panel Boards of Street Lighting Network-[Road 10]	12	15-Apr-27	28-Apr-27	09-Jun-26	22-Jun-26	0%	5,660	5,660
Medium Voltage Network		7	13-Oct-26	20-Oct-26	09-Sep-26	16-Sep-26	0%	0	0
Termination and Testing Works		7	13-Oct-26	20-Oct-26	09-Sep-26	16-Sep-26	0%	0	0
CO-R10-MV-TF-14	Termination Works of Medium Voltage Network-[Road 10]	7	13-Oct-26	20-Oct-26	09-Sep-26	16-Sep-26	0%	0	0
Road Works		25	12-Jul-27	09-Aug-27	30-Sep-26	31-Oct-26	0%	2,156,925	2,156,925
Bituminous Construction		13	12-Jul-27	26-Jul-27	30-Sep-26	17-Oct-26	0%	2,064,315	2,064,315
CO-R10-S03-RD-I	Application of Prime Coat Layer for Road Works- S.W 05-[Road 10]	10	12-Jul-27	22-Jul-27	30-Sep-26	11-Oct-26	0%	577,777	577,777
CO-R10-S04-RD-I	Application of Prime Coat Layer for Road Works- S.W 06-[Road 10]	10	12-Jul-27	22-Jul-27	03-Oct-26	13-Oct-26	0%	577,777	577,777
CO-R10-S03-RD-F-	Bituminous Base & Wearing Courses Layers for Road Works- S.W 05-[Road 10]	10	15-Jul-27	26-Jul-27	04-Oct-26	14-Oct-26	0%	454,381	454,381
CO-R10-S04-RD-F-	Bituminous Base & Wearing Courses Layers for Road Works- S.W 06-[Road 10]	10	15-Jul-27	26-Jul-27	06-Oct-26	17-Oct-26	0%	454,381	454,381
Traffic Signs Boards and Roads Marking		12	27-Jul-27	09-Aug-27	15-Oct-26	31-Oct-26	0%	92,610	92,610
CO-R10-S03-RD-I	Application of Road Marking Works For Road Works- S.W 05-[Road 10]	12	27-Jul-27	09-Aug-27	15-Oct-26	28-Oct-26	0%	33,688	33,688
CO-R10-S03-RD-I	Installation Works of Traffic Signs Boards For Road Works- S.W 05-[Road 10]	12	27-Jul-27	09-Aug-27	15-Oct-26	28-Oct-26	0%	12,617	12,617
CO-R10-S04-RD-I	Application of Road Marking Works For Road Works- S.W 06-[Road 10]	12	27-Jul-27	09-Aug-27	18-Oct-26	31-Oct-26	0%	33,688	33,688
CO-R10-S04-RD-I	Installation Works of Traffic Signs Boards For Road Works- S.W 06-[Road 10]	10	29-Jul-27	09-Aug-27	20-Oct-26	31-Oct-26	0%	12,617	12,617
Road 11 Local 1 (670 LM)		302	22-Jun-26 A	21-Aug-27	18-May-26	11-Nov-26	26.99%	815,107	815,107
Sewage Network		27	12-May-27	17-Jun-27	12-Aug-26	12-Sep-26	0%	210,240	210,240
Testing and Finishes		27	12-May-27	17-Jun-27	12-Aug-26	12-Sep-26	0%	210,240	210,240
CO-R11-SW-TF-1(	Final Testing For Main Line of Sewage Network-[Road 11]	12	12-May-27	31-May-27	12-Aug-26	25-Aug-26	0%	181,391	181,391
CO-R11-SW-TF-110	Install Manhole Cover Works for External Finishes of Sewage Network-[Road 11]	12	01-Jun-27	14-Jun-27	26-Aug-26	08-Sep-26	0%	14,425	14,425
CO-R11-SW-TF-130	Main Manhole Internal Finishes (Benching + Insulation) of Sewage Network-[Road 11]	12	05-Jun-27	17-Jun-27	30-Aug-26	12-Sep-26	0%	14,425	14,425
Storm Drainage Network		35	22-Jun-26 A	14-Jun-27	23-Aug-26	03-Oct-26	81.11%	271,250	271,250
Testing and Finishes		35	22-Jun-26 A	14-Jun-27	23-Aug-26	03-Oct-26	81.11%	271,250	271,250

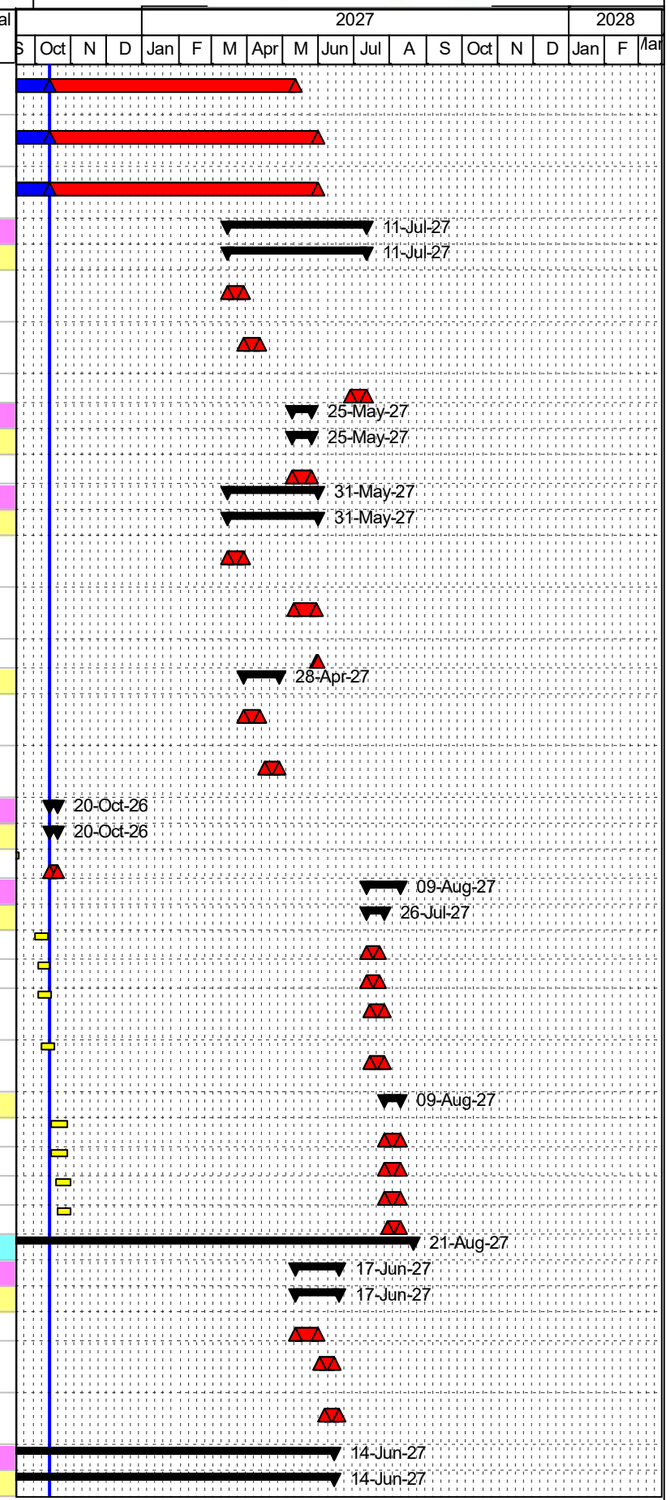

Primary Baseline
Actual Work
Summary
Remaining Work
Baseline Milestone
Critical Remaining Work
Milestone

Date	Revision	Checked	Approved
13-Oct-26	Third Industrial City		


Activity ID	Activity Name	Original Duration	Start	Finish	BL Project Start	BL Project Finish	Performance % Complete	Budgeted Total Cost	Remaining Total Cost
CO-R11-SD-TF-130	Catch Basin Internal Finishes (Benching + Insulation) for Storm Drainage Network-[Road 11]	16	22-Jun-26 A	14-Jun-27	14-Sep-26	03-Oct-26	20%	8,112	8,112
CO-R11-SD-TF-120	Main Manhole Internal Finishes (Benching + Insulation) for Storm Drainage Network-[Road 11]	12	23-Jun-26 A	14-Jun-27	09-Sep-26	22-Sep-26	85%	255,027	255,027
CO-R11-SD-TF-110	Install Catch Basin Cover Works for External Finishes of Storm Drainage Network-[Road 11]	12	27-Jun-26 A	06-May-27	23-Aug-26	05-Sep-26	20%	8,112	8,112
Potable Water Network		97	29-Mar-27	25-Jul-27	26-Aug-26	22-Sep-26	0%	11,619	11,619
Testing and Finishes		97	29-Mar-27	25-Jul-27	26-Aug-26	22-Sep-26	0%	11,619	11,619
CO-R11-PW-TF-100	Final Finishes works and Covers for Valves and Valve Chambers of Potable Water Network-[Road 11]	12	29-Mar-27	11-Apr-27	26-Aug-26	08-Sep-26	0%	0	0
CO-R11-PW-TF-120	Fire Hydrant Finishies (S.Box + Safety + Marker Post) of Potable Water Network-[Road 11]	12	12-Apr-27	25-Apr-27	09-Sep-26	22-Sep-26	0%	0	0
CO-R11-PW-TF-11	Testing Work for Main Line of Potable Water Network-[Road 11]	12	12-Jul-27	25-Jul-27	26-Aug-26	08-Sep-26	0%	11,619	11,619
Irrigation Network		10	26-May-27	06-Jun-27	23-Aug-26	02-Sep-26	0%	6,235	6,235
Testing and Finishes		10	26-May-27	06-Jun-27	23-Aug-26	02-Sep-26	0%	6,235	6,235
CO-R11-IR-TF-13(	Final Testing (pressure tests) of Irrigation Network-[Road 11]	10	26-May-27	06-Jun-27	23-Aug-26	02-Sep-26	0%	6,235	6,235
Street Lighting Network		40	20-Jun-27	04-Aug-27	18-May-26	10-Aug-26	0%	23,933	23,933
Termination and Testing Works		40	20-Jun-27	04-Aug-27	18-May-26	10-Aug-26	0%	23,933	23,933
CO-R11-SL-TF-160	Termination Works For Lighting Poles Cables of Street Lighting Network-[Road 11]	12	20-Jun-27	03-Jul-27	18-May-26	04-Jun-26	0%	23,933	23,933
CO-R11-SL-TF-170	Termination Works For Panel Board Cables of Street Lighting Network-[Road 11]	12	20-Jul-27	02-Aug-27	26-Jul-26	08-Aug-26	0%	0	0
CO-R11-SL-TF-38(	Testing Works For Panel Board Cables of Street Lighting Network-[Road 11]	2	03-Aug-27	04-Aug-27	09-Aug-26	10-Aug-26	0%	0	0
Medium Voltage Network		7	12-Jan-27	19-Jan-27	17-Sep-26	26-Sep-26	0%	0	0
Termination and Testing Works		7	12-Jan-27	19-Jan-27	17-Sep-26	26-Sep-26	0%	0	0
CO-R11-MV-TF-1(	Termination Works of Medium Voltage Network-[Road 11]	7	12-Jan-27	19-Jan-27	17-Sep-26	26-Sep-26	0%	0	0
Road Works		22	27-Jul-27	21-Aug-27	15-Oct-26	11-Nov-26	0%	291,830	291,830
Bituminous Construction		12	27-Jul-27	09-Aug-27	15-Oct-26	31-Oct-26	0%	265,183	265,183
CO-R11-S05-RD-F-(	Bituminous Base & Wearing Courses Layers for Road Works- S.W 07-[Road 11]	12	27-Jul-27	09-Aug-27	15-Oct-26	28-Oct-26	0%	132,592	132,592
CO-R11-S06-RD-F-(	Bituminous Base & Wearing Courses Layers for Road Works- S.W 08-[Road 11]	12	27-Jul-27	09-Aug-27	18-Oct-26	31-Oct-26	0%	132,592	132,592
Traffic Signs Boards and Roads Marking		10	10-Aug-27	21-Aug-27	29-Oct-26	11-Nov-26	0%	26,647	26,647
CO-R11-S05-RD-F	Application of Road Marking Works For Road Works- S.W 07-[Road 11]	10	10-Aug-27	21-Aug-27	29-Oct-26	09-Nov-26	0%	9,830	9,830
CO-R11-S05-RD-F	Installation Works of Traffic Signs Boards For Road Works- S.W 07-[Road 11]	10	10-Aug-27	21-Aug-27	29-Oct-26	09-Nov-26	0%	3,493	3,493
CO-R11-S06-RD-F	Application of Road Marking Works For Road Works- S.W 08-[Road 11]	10	10-Aug-27	21-Aug-27	01-Nov-26	11-Nov-26	0%	9,830	9,830
CO-R11-S06-RD-F	Installation Works of Traffic Signs Boards For Road Works- S.W 08-[Road 11]	10	10-Aug-27	21-Aug-27	01-Nov-26	11-Nov-26	0%	3,493	3,493
Road 14 Local 1 (584 LM)		195	20-Jan-27	14-Sep-27	13-Jun-26	23-Nov-26	0%	1,081,359	1,081,359
Sewage Network		27	01-Jun-27	01-Jul-27	26-Aug-26	27-Sep-26	0%	48,450	48,450
Testing and Finishes		27	01-Jun-27	01-Jul-27	26-Aug-26	27-Sep-26	0%	48,450	48,450
CO-R14-SW-TF-1(	Final Testing For Main Line of Sewage Network-[Road 14]	12	01-Jun-27	14-Jun-27	26-Aug-26	08-Sep-26	0%	31,128	31,128
CO-R14-SW-TF-110	Install Manhole Cover Works for External Finishes of Sewage Network-[Road 14]	12	15-Jun-27	28-Jun-27	09-Sep-26	22-Sep-26	0%	8,661	8,661
CO-R14-SW-TF-130	Main Manhole Internal Finishes (Benching + Insulation) of Sewage Network-[Road 14]	12	19-Jun-27	01-Jul-27	13-Sep-26	27-Sep-26	0%	8,661	8,661
Potable Water Network		97	12-Apr-27	08-Aug-27	09-Sep-26	07-Oct-26	0%	44,448	44,448
Testing and Finishes		97	12-Apr-27	08-Aug-27	09-Sep-26	07-Oct-26	0%	44,448	44,448
CO-R14-PW-TF-100	Final Finishes works and Covers for Valves and Valve Chambers of Potable Water Network-[Road 14]	12	12-Apr-27	25-Apr-27	09-Sep-26	22-Sep-26	0%	0	0
CO-R14-PW-TF-120	Fire Hydrant Finishies (S.Box + Safety + Marker Post) of Potable Water Network-[Road 14]	12	26-Apr-27	09-May-27	24-Sep-26	07-Oct-26	0%	0	0
CO-R14-PW-TF-1(	Testing Work for Main Line of Potable Water Network-[Road 14]	12	26-Jul-27	08-Aug-27	09-Sep-26	22-Sep-26	0%	44,448	44,448
Irrigation Network		10	07-Jun-27	17-Jun-27	03-Sep-26	14-Sep-26	0%	24,385	24,385
Testing and Finishes		10	07-Jun-27	17-Jun-27	03-Sep-26	14-Sep-26	0%	24,385	24,385
CO-R11-IR-TF-14(	Final Testing (pressure tests) of Irrigation Network-[Road 14]	10	07-Jun-27	17-Jun-27	03-Sep-26	14-Sep-26	0%	24,385	24,385

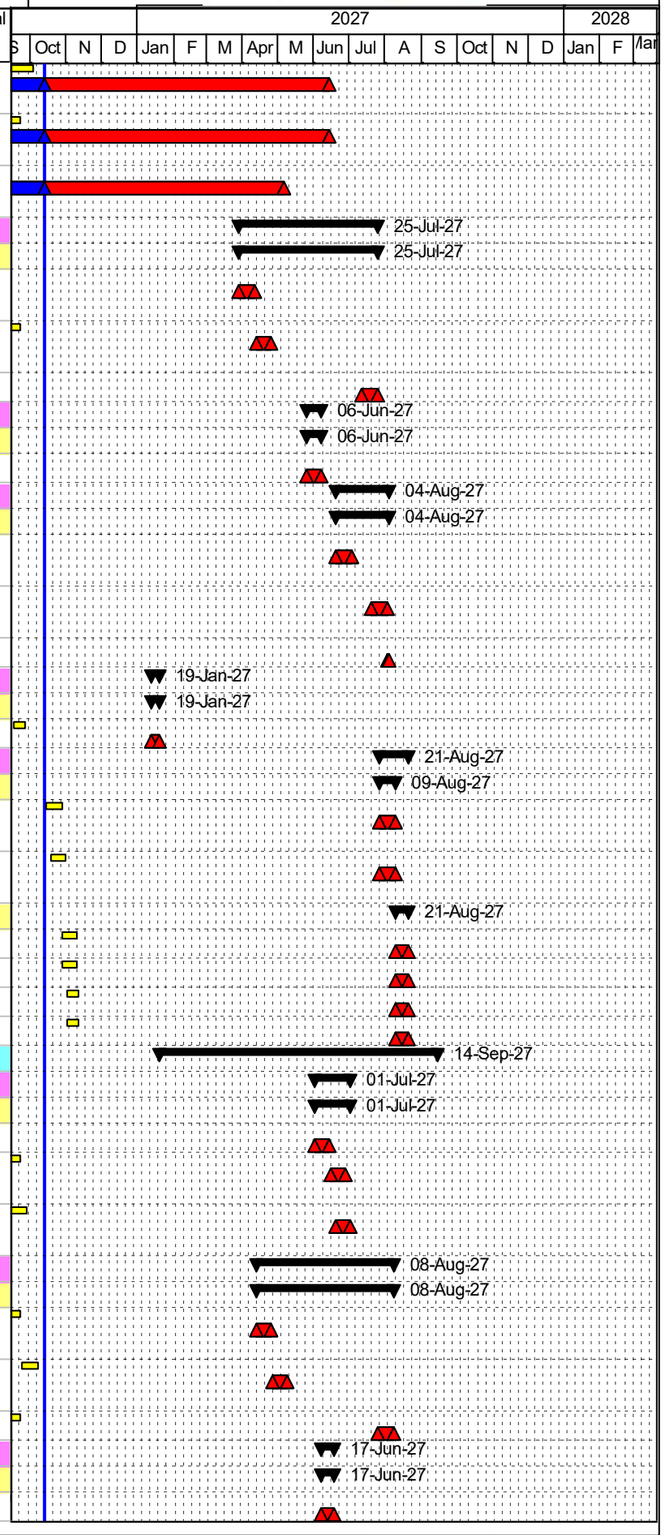

Primary Baseline | Actual Work | Summary
Remaining Work | Baseline Milestone
Critical Remaining Work | Milestone

Date	Revision	Checked	Approved
13-Oct-26	Third Industrial City		


Activity ID	Activity Name	Original Duration	Start	Finish	BL Project Start	BL Project Finish	Performance % Complete	Budgeted Total Cost	Remaining Total Cost
Street Lighting Network		40	04-Jul-27	18-Aug-27	13-Jun-26	31-Aug-26	0%	34,865	34,865
Termination and Testing Works		40	04-Jul-27	18-Aug-27	13-Jun-26	31-Aug-26	0%	34,865	34,865
CO-R11-SL-TF-180	Termination Works For Lighting Poles Cables of Street Lighting Network-[Road 14]	12	04-Jul-27	17-Jul-27	13-Jun-26	25-Jun-26	0%	34,865	34,865
CO-R11-SL-TF-190	Termination Works For Panel Board Cables of Street Lighting Network-[Road 14]	12	03-Aug-27	16-Aug-27	16-Aug-26	29-Aug-26	0%	0	0
CO-R14-SL-TF-38	Testing Works For Panel Board Cables of Street Lighting Network-[Road 14]	2	17-Aug-27	18-Aug-27	30-Aug-26	31-Aug-26	0%	0	0
Medium Voltage Network		7	20-Jan-27	27-Jan-27	27-Sep-26	04-Oct-26	0%	0	0
Termination and Testing Works		7	20-Jan-27	27-Jan-27	27-Sep-26	04-Oct-26	0%	0	0
CO-R11-MV-TF-1	Termination Works of Medium Voltage Network-[Road 14]	7	20-Jan-27	27-Jan-27	27-Sep-26	04-Oct-26	0%	0	0
Road Works		25	17-Aug-27	14-Sep-27	26-Oct-26	23-Nov-26	0%	929,210	929,210
Bituminous Construction		15	17-Aug-27	02-Sep-27	26-Oct-26	11-Nov-26	0%	888,935	888,935
CO-R11-S07-RD-F	Application of Prime Coat Layer for Road Works- S.W 09-[Road 14]	12	17-Aug-27	30-Aug-27	26-Oct-26	08-Nov-26	0%	248,802	248,802
CO-R11-S08-RD-F	Application of Prime Coat Layer for Road Works- S.W 10-[Road 14]	10	17-Aug-27	28-Aug-27	28-Oct-26	08-Nov-26	0%	248,802	248,802
CO-R11-S07-RD-F-	Bituminous Base & Wearing Courses Layers for Road Works- S.W 09-[Road 14]	10	23-Aug-27	02-Sep-27	01-Nov-26	11-Nov-26	0%	195,665	195,665
CO-R11-S08-RD-F-	Bituminous Base & Wearing Courses Layers for Road Works- S.W 10-[Road 14]	10	23-Aug-27	02-Sep-27	01-Nov-26	11-Nov-26	0%	195,665	195,665
Traffic Signs Boards and Roads Marking		12	01-Sep-27	14-Sep-27	10-Nov-26	23-Nov-26	0%	40,275	40,275
CO-R11-S07-RD-F	Installation Works of Traffic Signs Boards For Road Works- S.W 09-[Road 14]	12	01-Sep-27	14-Sep-27	10-Nov-26	23-Nov-26	0%	5,631	5,631
CO-R11-S07-RD-F	Application of Road Marking Works For Road Works- S.W 09-[Road 14]	10	04-Sep-27	14-Sep-27	12-Nov-26	23-Nov-26	0%	14,507	14,507
CO-R11-S08-RD-F	Application of Road Marking Works For Road Works- S.W 10-[Road 14]	10	04-Sep-27	14-Sep-27	12-Nov-26	23-Nov-26	0%	14,507	14,507
CO-R11-S08-RD-F	Installation Works of Traffic Signs Boards For Road Works- S.W 10-[Road 14]	10	04-Sep-27	14-Sep-27	12-Nov-26	23-Nov-26	0%	5,631	5,631
Road 15 Local 1 (556 LM)		239	14-Dec-26	29-Sep-27	27-Jun-26	07-Dec-26	0%	117,781	117,781
Sewage Network		27	15-Jun-27	15-Jul-27	09-Sep-26	11-Oct-26	0%	44,915	44,915
Testing and Finishes		27	15-Jun-27	15-Jul-27	09-Sep-26	11-Oct-26	0%	44,915	44,915
CO-R15-SW-TF-1(	Final Testing For Main Line of Sewage Network-[Road 15]	12	15-Jun-27	28-Jun-27	09-Sep-26	22-Sep-26	0%	20,768	20,768
CO-R15-SW-TF-110	Install Manhole Cover Works for External Finishes of Sewage Network-[Road 15]	12	29-Jun-27	12-Jul-27	24-Sep-26	07-Oct-26	0%	12,073	12,073
CO-R15-SW-TF-130	Main Manhole Internal Finishes (Benching + Insulation) of Sewage Network-[Road 15]	12	03-Jul-27	15-Jul-27	28-Sep-26	11-Oct-26	0%	12,073	12,073
Storm Drainage Network		188	14-Dec-26	31-Jul-27	20-Sep-26	09-Nov-26	0%	13,655	13,655
Testing and Finishes		188	14-Dec-26	31-Jul-27	20-Sep-26	09-Nov-26	0%	13,655	13,655
CO-R15-SD-TF-110	Install Catch Basin Cover Works for External Finishes of Storm Drainage Network-[Road 15]	12	14-Dec-26	27-Dec-26	20-Sep-26	04-Oct-26	0%	6,827	6,827
CO-R15-SD-TF-130	Catch Basin Internal Finishes (Benching + Insulation) for Storm Drainage Network-[Road 15]	16	13-Jul-27	31-Jul-27	22-Oct-26	09-Nov-26	0%	6,827	6,827
Potable Water Network		97	26-Apr-27	22-Aug-27	24-Sep-26	21-Oct-26	0%	9,843	9,843
Testing and Finishes		97	26-Apr-27	22-Aug-27	24-Sep-26	21-Oct-26	0%	9,843	9,843
CO-R15-PW-TF-100	Final Finishes works and Covers for Valves and Valve Chambers of Potable Water Network-[Road 15]	12	26-Apr-27	09-May-27	24-Sep-26	07-Oct-26	0%	0	0
CO-R15-PW-TF-120	Fire Hydrant Finishies (S.Box + Safety + Marker Post) of Potable Water Network-[Road 15]	12	10-May-27	29-May-27	08-Oct-26	21-Oct-26	0%	0	0
CO-R15-PW-TF-1	Testing Work for Main Line of Potable Water Network-[Road 15]	12	09-Aug-27	22-Aug-27	24-Sep-26	07-Oct-26	0%	9,843	9,843
Irrigation Network		10	19-Jun-27	29-Jun-27	15-Sep-26	27-Sep-26	0%	5,248	5,248
Testing and Finishes		10	19-Jun-27	29-Jun-27	15-Sep-26	27-Sep-26	0%	5,248	5,248
CO-R15-IR-TF-15(	Final Testing (pressure tests) of Irrigation Network-[Road 15]	10	19-Jun-27	29-Jun-27	15-Sep-26	27-Sep-26	0%	5,248	5,248
Street Lighting Network		56	18-Jul-27	20-Sep-27	27-Jun-26	04-Oct-26	0%	20,092	20,092
Termination and Testing Works		56	18-Jul-27	20-Sep-27	27-Jun-26	04-Oct-26	0%	20,092	20,092
CO-R15-SL-TF-200	Termination Works For Lighting Poles Cables of Street Lighting Network-[Road 15]	12	18-Jul-27	31-Jul-27	27-Jun-26	09-Jul-26	0%	20,092	20,092
CO-R15-SL-TF-210	Termination Works For Panel Board Cables of Street Lighting Network-[Road 15]	12	19-Aug-27	01-Sep-27	01-Sep-26	14-Sep-26	0%	0	0
CO-R15-SL-TF-38	Testing Works For Panel Board Cables of Street Lighting Network-[Road 15]	16	02-Sep-27	20-Sep-27	15-Sep-26	04-Oct-26	0%	0	0
Medium Voltage Network		7	28-Jan-27	04-Feb-27	05-Oct-26	12-Oct-26	0%	0	0

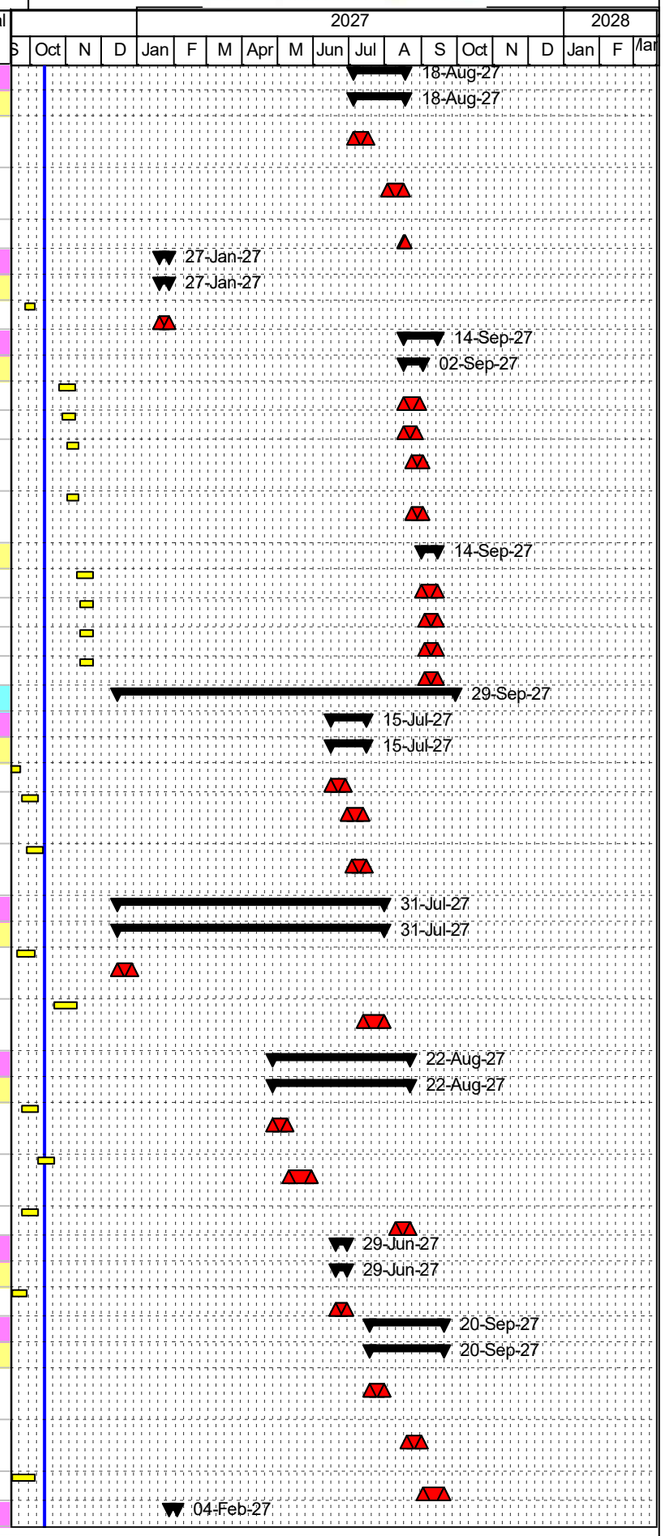

Primary Baseline · Actual Work · Summary
Remaining Work · Baseline Milestone
Critical Remaining Work · Milestone

Date	Revision	Checked	Approved
13-Oct-26	Third Industrial City		


Activity ID	Activity Name	Original Duration	Start	Finish	BL Project Start	BL Project Finish	Performance % Complete	Budgeted Total Cost	Remaining Total Cost
Termination and Testing Works		7	28-Jan-27	04-Feb-27	05-Oct-26	12-Oct-26	0%	0	0
CO-R15-MV-TF-20	Termination Works of Medium Voltage Network-[Road 15]	7	28-Jan-27	04-Feb-27	05-Oct-26	12-Oct-26	0%	0	0
Road Works		12	15-Sep-27	29-Sep-27	24-Nov-26	07-Dec-26	0%	24,029	24,029
Traffic Signs Boards and Roads Marking		12	15-Sep-27	29-Sep-27	24-Nov-26	07-Dec-26	0%	24,029	24,029
CO-R15-S09-RD-I	Application of Road Marking Works For Road Works- S.W 11-[Road 15]	10	15-Sep-27	27-Sep-27	24-Nov-26	05-Dec-26	0%	8,274	8,274
CO-R15-S09-RD-I	Installation Works of Traffic Signs Boards For Road Works- S.W 11-[Road 15]	10	15-Sep-27	27-Sep-27	24-Nov-26	05-Dec-26	0%	3,302	3,302
CO-R15-S10-RD-I	Application of Road Marking Works For Road Works- S.W 12-[Road 15]	10	15-Sep-27	27-Sep-27	24-Nov-26	05-Dec-26	0%	8,274	8,274
CO-R15-S10-RD-I	Installation Works of Traffic Signs Boards For Road Works- S.W 12-[Road 15]	12	15-Sep-27	29-Sep-27	24-Nov-26	07-Dec-26	0%	4,179	4,179
Road 16 Local 1 (527 LM)		279	09-Nov-26	11-Oct-27	11-Jul-26	19-Dec-26	0%	163,354	163,354
Sewage Network		27	29-Jun-27	29-Jul-27	24-Sep-26	25-Oct-26	0%	28,933	28,933
Testing and Finishes		27	29-Jun-27	29-Jul-27	24-Sep-26	25-Oct-26	0%	28,933	28,933
CO-R16-SW-TF-10	Final Testing For Main Line of Sewage Network-[Road 16]	12	29-Jun-27	12-Jul-27	24-Sep-26	07-Oct-26	0%	14,883	14,883
CO-R16-SW-TF-110	Install Manhole Cover Works for External Finishes of Sewage Network-[Road 16]	12	13-Jul-27	26-Jul-27	08-Oct-26	21-Oct-26	0%	7,025	7,025
CO-R16-SW-TF-130	Main Manhole Internal Finishes (Benching + Insulation) of Sewage Network-[Road 16]	12	17-Jul-27	29-Jul-27	12-Oct-26	25-Oct-26	0%	7,025	7,025
Storm Drainage Network		234	09-Nov-26	18-Aug-27	10-Sep-26	28-Nov-26	0%	78,486	78,486
Testing and Finishes		234	09-Nov-26	18-Aug-27	10-Sep-26	28-Nov-26	0%	78,486	78,486
CO-R16-SD-TF-10	Testing Work for Pipes of Storm Drainage Network-[Road 16]	16	09-Nov-26	26-Nov-26	10-Sep-26	29-Sep-26	0%	65,472	65,472
CO-R16-SD-TF-110	Install Catch Basin Cover Works for External Finishes of Storm Drainage Network-[Road 16]	12	28-Dec-26	10-Jan-27	05-Oct-26	18-Oct-26	0%	6,507	6,507
CO-R16-SD-TF-130	Catch Basin Internal Finishes (Benching + Insulation) for Storm Drainage Network-[Road 16]	16	01-Aug-27	18-Aug-27	10-Nov-26	28-Nov-26	0%	6,507	6,507
Potable Water Network		97	10-May-27	05-Sep-27	08-Oct-26	04-Nov-26	0%	9,456	9,456
Testing and Finishes		97	10-May-27	05-Sep-27	08-Oct-26	04-Nov-26	0%	9,456	9,456
CO-R16-PW-TF-100	Final Finishes works and Covers for Valves and Valve Chambers of Potable Water Network-[Road 16]	12	10-May-27	29-May-27	08-Oct-26	21-Oct-26	0%	0	0
CO-R16-PW-TF-120	Fire Hydrant Finishies (S.Box + Safety + Marker Post) of Potable Water Network-[Road 16]	12	30-May-27	12-Jun-27	22-Oct-26	04-Nov-26	0%	0	0
CO-R16-PW-TF-1	Testing Work for Main Line of Potable Water Network-[Road 16]	12	23-Aug-27	05-Sep-27	08-Oct-26	21-Oct-26	0%	9,456	9,456
Irrigation Network		10	30-Jun-27	11-Jul-27	28-Sep-26	08-Oct-26	0%	5,002	5,002
Testing and Finishes		10	30-Jun-27	11-Jul-27	28-Sep-26	08-Oct-26	0%	5,002	5,002
CO-R16-IR-TF-16(	Final Testing (pressure tests) of Irrigation Network-[Road 16]	10	30-Jun-27	11-Jul-27	28-Sep-26	08-Oct-26	0%	5,002	5,002
Street Lighting Network		46	01-Aug-27	22-Sep-27	11-Jul-26	06-Oct-26	0%	18,910	18,910
Termination and Testing Works		46	01-Aug-27	22-Sep-27	11-Jul-26	06-Oct-26	0%	18,910	18,910
CO-R16-SL-TF-220	Termination Works For Lighting Poles Cables of Street Lighting Network-[Road 16]	12	01-Aug-27	14-Aug-27	11-Jul-26	23-Jul-26	0%	18,910	18,910
CO-R16-SL-TF-230	Termination Works For Panel Board Cables of Street Lighting Network-[Road 16]	12	02-Sep-27	15-Sep-27	15-Sep-26	29-Sep-26	0%	0	0
CO-R16-SL-TF-38	Testing Works For Panel Board Cables of Street Lighting Network-[Road 16]	2	21-Sep-27	22-Sep-27	05-Oct-26	06-Oct-26	0%	0	0
Medium Voltage Network		7	06-Feb-27	13-Feb-27	13-Oct-26	20-Oct-26	0%	0	0
Termination and Testing Works		7	06-Feb-27	13-Feb-27	13-Oct-26	20-Oct-26	0%	0	0
CO-R16-MV-TF-22	Termination Works of Medium Voltage Network-[Road 16]	7	06-Feb-27	13-Feb-27	13-Oct-26	20-Oct-26	0%	0	0
Road Works		12	28-Sep-27	11-Oct-27	06-Dec-26	19-Dec-26	0%	22,567	22,567
Traffic Signs Boards and Roads Marking		12	28-Sep-27	11-Oct-27	06-Dec-26	19-Dec-26	0%	22,567	22,567
CO-R16-S11-RD-I	Application of Road Marking Works For Road Works- S.W 13-[Road 16]	10	28-Sep-27	09-Oct-27	06-Dec-26	16-Dec-26	0%	7,886	7,886
CO-R16-S11-RD-I	Installation Works of Traffic Signs Boards For Road Works- S.W 13-[Road 16]	10	28-Sep-27	09-Oct-27	06-Dec-26	16-Dec-26	0%	3,398	3,398
CO-R16-S12-RD-I	Application of Road Marking Works For Road Works- S.W 14-[Road 16]	10	28-Sep-27	09-Oct-27	06-Dec-26	16-Dec-26	0%	7,886	7,886
CO-R16-S12-RD-I	Installation Works of Traffic Signs Boards For Road Works- S.W 14-[Road 16]	10	30-Sep-27	11-Oct-27	08-Dec-26	19-Dec-26	0%	3,398	3,398
Road 17 Local 1 (500 LM)		271	28-Nov-26	20-Oct-27	25-Jul-26	28-Dec-26	0%	145,258	145,258
Sewage Network		27	13-Jul-27	12-Aug-27	08-Oct-26	08-Nov-26	0%	28,783	28,783
Testing and Finishes		27	13-Jul-27	12-Aug-27	08-Oct-26	08-Nov-26	0%	28,783	28,783
CO-R17-SW-TF-1(	Final Testing For Main Line of Sewage Network-[Road 17]	12	13-Jul-27	26-Jul-27	08-Oct-26	21-Oct-26	0%	15,595	15,595

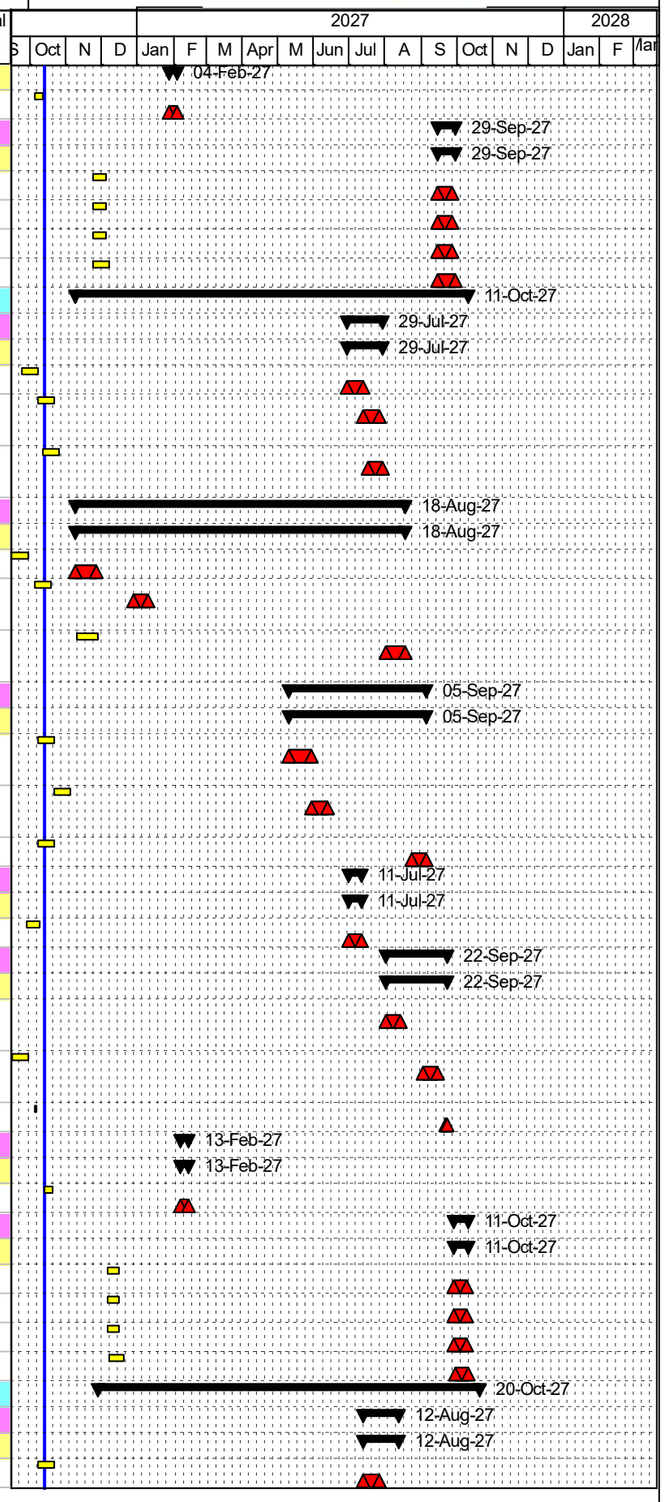

Primary Baseline | Actual Work | Summary
Remaining Work | Baseline Milestone
Critical Remaining Work | Milestone

Date	Revision	Checked	Approved
13-Oct-26	Third Industrial City		


Activity ID	Activity Name	Original Duration	Start	Finish	BL Project Start	BL Project Finish	Performance % Complete	Budgeted Total Cost	Remaining Total Cost
CO-R17-SW-TF-110	Install Manhole Cover Works for External Finishes of Sewage Network-[Road 17]	12	27-Jul-27	09-Aug-27	22-Oct-26	04-Nov-26	0%	6,594	6,594
CO-R17-SW-TF-130	Main Manhole Internal Finishes (Benching + Insulation) of Sewage Network-[Road 17]	12	31-Jul-27	12-Aug-27	26-Oct-26	08-Nov-26	0%	6,594	6,594
Storm Drainage Network		230	28-Nov-26	01-Sep-27	04-Oct-26	12-Dec-26	0%	64,596	64,596
Testing and Finishes		230	28-Nov-26	01-Sep-27	04-Oct-26	12-Dec-26	0%	64,596	64,596
CO-R17-SD-TF-1(	Testing Work for Pipes of Storm Drainage Network-[Road 17]	16	28-Nov-26	15-Dec-26	04-Oct-26	21-Oct-26	0%	52,222	52,222
CO-R17-SD-TF-110	Install Catch Basin Cover Works for External Finishes of Storm Drainage Network-[Road 17]	12	11-Jan-27	24-Jan-27	19-Oct-26	01-Nov-26	0%	6,187	6,187
CO-R17-SD-TF-130	Catch Basin Internal Finishes (Benching + Insulation) for Storm Drainage Network-[Road 17]	12	19-Aug-27	01-Sep-27	29-Nov-26	12-Dec-26	0%	6,187	6,187
Potable Water Network		97	30-May-27	19-Sep-27	22-Oct-26	18-Nov-26	0%	9,063	9,063
Testing and Finishes		97	30-May-27	19-Sep-27	22-Oct-26	18-Nov-26	0%	9,063	9,063
CO-R17-PW-TF-100	Final Finishes works and Covers for Valves and Valve Chambers of Potable Water Network-[Road 17]	12	30-May-27	12-Jun-27	22-Oct-26	04-Nov-26	0%	0	0
CO-R17-PW-TF-120	Fire Hydrant Finishies (S.Box + Safety + Marker Post) of Potable Water Network-[Road 17]	12	13-Jun-27	26-Jun-27	05-Nov-26	18-Nov-26	0%	0	0
CO-R17-PW-TF-1(	Testing Work for Main Line of Potable Water Network-[Road 17]	12	06-Sep-27	19-Sep-27	22-Oct-26	04-Nov-26	0%	9,063	9,063
Irrigation Network		10	12-Jul-27	22-Jul-27	18-Oct-26	28-Oct-26	0%	4,756	4,756
Testing and Finishes		10	12-Jul-27	22-Jul-27	18-Oct-26	28-Oct-26	0%	4,756	4,756
CO-R17-IR-TF-17(	Final Testing (pressure tests) of Irrigation Network-[Road 17]	10	12-Jul-27	22-Jul-27	18-Oct-26	28-Oct-26	0%	4,756	4,756
Street Lighting Network		42	15-Aug-27	03-Oct-27	25-Jul-26	15-Oct-26	0%	18,024	18,024
Termination and Testing Works		42	15-Aug-27	03-Oct-27	25-Jul-26	15-Oct-26	0%	18,024	18,024
CO-R17-SL-TF-240	Termination Works For Lighting Poles Cables of Street Lighting Network-[Road 17]	12	15-Aug-27	28-Aug-27	25-Jul-26	06-Aug-26	0%	18,024	18,024
CO-R17-SL-TF-250	Termination Works For Panel Board Cables of Street Lighting Network-[Road 17]	12	16-Sep-27	30-Sep-27	30-Sep-26	13-Oct-26	0%	0	0
CO-R17-SL-TF-38	Testing Works For Panel Board Cables of Street Lighting Network-[Road 17]	2	02-Oct-27	03-Oct-27	14-Oct-26	15-Oct-26	0%	0	0
Medium Voltage Network		7	14-Feb-27	21-Feb-27	21-Oct-26	28-Oct-26	0%	0	0
Termination and Testing Works		7	14-Feb-27	21-Feb-27	21-Oct-26	28-Oct-26	0%	0	0
CO-R17-MV-TF-24	Termination Works of Medium Voltage Network-[Road 17]	7	14-Feb-27	21-Feb-27	21-Oct-26	28-Oct-26	0%	0	0
Road Works		10	10-Oct-27	20-Oct-27	17-Dec-26	28-Dec-26	0%	20,037	20,037
Traffic Signs Boards and Roads Marking		10	10-Oct-27	20-Oct-27	17-Dec-26	28-Dec-26	0%	20,037	20,037
CO-R17-S13-RD-I	Application of Road Marking Works For Road Works- S.W 15-[Road 17]	10	10-Oct-27	20-Oct-27	17-Dec-26	28-Dec-26	0%	7,498	7,498
CO-R17-S13-RD-I	Installation Works of Traffic Signs Boards For Road Works- S.W 15-[Road 17]	10	10-Oct-27	20-Oct-27	17-Dec-26	28-Dec-26	0%	2,521	2,521
CO-R17-S14-RD-I	Application of Road Marking Works For Road Works- S.W 16-[Road 17]	10	10-Oct-27	20-Oct-27	17-Dec-26	28-Dec-26	0%	7,498	7,498
CO-R17-S14-RD-I	Installation Works of Traffic Signs Boards For Road Works- S.W 16-[Road 17]	7	13-Oct-27	20-Oct-27	21-Dec-26	28-Dec-26	0%	2,521	2,521
Road 18 Local 1 (479 LM)		231	02-Mar-27	06-Dec-27	16-Jun-26	19-Dec-26	0%	164,388	164,388
Sewage Network		27	12-Jun-27	12-Jul-27	20-Aug-26	16-Sep-26	0%	29,759	29,759
Testing and Finishes		27	12-Jun-27	12-Jul-27	20-Aug-26	16-Sep-26	0%	29,759	29,759
CO-R18-SW-TF-1(	Final Testing For Main Line of Sewage Network-[Road 18]	12	12-Jun-27	24-Jun-27	20-Aug-26	02-Sep-26	0%	12,907	12,907
CO-R18-SW-TF-110	Install Manhole Cover Works for External Finishes of Sewage Network-[Road 18]	12	26-Jun-27	08-Jul-27	03-Sep-26	16-Sep-26	0%	8,426	8,426
CO-R18-SW-TF-130	Main Manhole Internal Finishes (Benching + Insulation) of Sewage Network-[Road 18]	12	29-Jun-27	12-Jul-27	03-Sep-26	16-Sep-26	0%	8,426	8,426
Storm Drainage Network		87	03-Apr-27	18-Jul-27	03-Aug-26	09-Nov-26	0%	81,227	81,227
Testing and Finishes		87	03-Apr-27	18-Jul-27	03-Aug-26	09-Nov-26	0%	81,227	81,227
CO-R18-SD-TF-110	Install Catch Basin Cover Works for External Finishes of Storm Drainage Network-[Road 18]	16	03-Apr-27	20-Apr-27	03-Aug-26	20-Aug-26	0%	5,983	5,983
CO-R18-SD-TF-1(	Testing Work for Pipes of Storm Drainage Network-[Road 18]	16	12-Jun-27	29-Jun-27	04-Oct-26	21-Oct-26	0%	69,262	69,262
CO-R18-SD-TF-130	Catch Basin Internal Finishes (Benching + Insulation) for Storm Drainage Network-[Road 18]	16	30-Jun-27	18-Jul-27	22-Oct-26	09-Nov-26	0%	5,983	5,983
Potable Water Network		72	12-Jul-27	04-Oct-27	26-Aug-26	18-Nov-26	0%	10,266	10,266
Testing and Finishes		72	12-Jul-27	04-Oct-27	26-Aug-26	18-Nov-26	0%	10,266	10,266

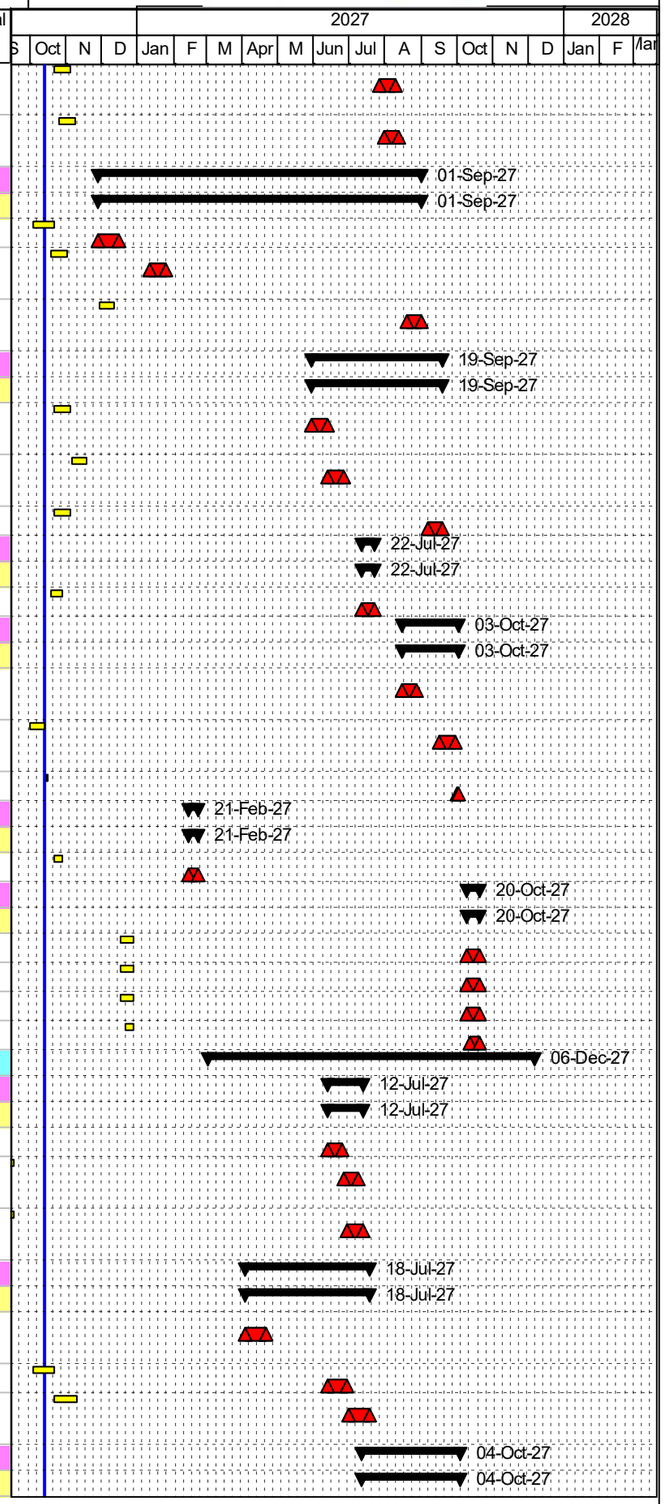

Primary Baseline
Remaining Work
Critical Remaining Work
Actual Work
Baseline Milestone
Milestone
Summary

Date	Revision	Checked	Approved
13-Oct-26	Third Industrial City		


Activity ID	Activity Name	Original Duration	Start	Finish	BL Project Start	BL Project Finish	Performance % Complete	Budgeted Total Cost	Remaining Total Cost
CO-R18-PW-TF-100	Final Finishes works and Covers for Valves and Valve Chambers of Potable Water Network-[Road 18]	12	12-Jul-27	25-Jul-27	26-Aug-26	08-Sep-26	0%	0	0
CO-R18-PW-TF-120	Fire Hydrant Finishies (S.Box + Safety + Marker Post) of Potable Water Network-[Road 18]	12	26-Jul-27	08-Aug-27	09-Sep-26	22-Sep-26	0%	0	0
CO-R18-PW-TF-1(	Testing Work for Main Line of Potable Water Network-[Road 18]	12	20-Sep-27	04-Oct-27	05-Nov-26	18-Nov-26	0%	10,266	10,266
Irrigation Network		16	27-Jun-27	14-Jul-27	17-Aug-26	03-Sep-26	0%	4,599	4,599
Testing and Finishes		16	27-Jun-27	14-Jul-27	17-Aug-26	03-Sep-26	0%	4,599	4,599
CO-R18-IR-TF-11(	Final Testing (pressure tests) of Irrigation Network-[Road 18]	16	27-Jun-27	14-Jul-27	17-Aug-26	03-Sep-26	0%	4,599	4,599
Street Lighting Network		76	17-Jun-27	13-Sep-27	16-Jun-26	12-Sep-26	0%	17,433	17,433
Termination and Testing Works		76	17-Jun-27	13-Sep-27	16-Jun-26	12-Sep-26	0%	17,433	17,433
CO-R18-SL-TF-120	Termination Works For Lighting Poles Cables of Street Lighting Network-[Road 18]	12	17-Jun-27	01-Jul-27	16-Jun-26	30-Jun-26	0%	17,433	17,433
CO-R18-SL-TF-130	Termination Works For Panel Board Cables of Street Lighting Network-[Road 18]	12	28-Aug-27	11-Sep-27	26-Aug-26	09-Sep-26	0%	0	0
CO-R18-SL-TF-38	Testing Works For Panel Board Cables of Street Lighting Network-[Road 18]	2	11-Sep-27	13-Sep-27	09-Sep-26	12-Sep-26	0%	0	0
Medium Voltage Network		16	02-Mar-27	23-Mar-27	09-Jul-26	27-Jul-26	0%	0	0
Termination and Testing Works		16	02-Mar-27	23-Mar-27	09-Jul-26	27-Jul-26	0%	0	0
CO-R18-MV-TF-12	Termination Works of Medium Voltage Network-[Road 18]	16	02-Mar-27	23-Mar-27	09-Jul-26	27-Jul-26	0%	0	0
Road Works		34	27-Oct-27	06-Dec-27	09-Nov-26	19-Dec-26	0%	21,105	21,105
Traffic Signs Boards and Roads Marking		34	27-Oct-27	06-Dec-27	09-Nov-26	19-Dec-26	0%	21,105	21,105
CO-R18-S15-RD-I	Application of Road Marking Works For Road Works- S.W 03-[Road 18]	12	27-Oct-27	10-Nov-27	09-Nov-26	23-Nov-26	0%	7,251	7,251
CO-R18-S15-RD-I	Installation Works of Traffic Signs Boards For Road Works- S.W 03-[Road 18]	12	10-Nov-27	24-Nov-27	23-Nov-26	07-Dec-26	0%	3,302	3,302
CO-R18-S16-RD-I	Application of Road Marking Works For Road Works- S.W 04-[Road 18]	15	10-Nov-27	28-Nov-27	30-Nov-26	17-Dec-26	0%	7,251	7,251
CO-R18-S16-RD-I	Installation Works of Traffic Signs Boards For Road Works- S.W 04-[Road 18]	10	24-Nov-27	06-Dec-27	07-Dec-26	19-Dec-26	0%	3,302	3,302
Independent Works		509	16-Sep-26 A	06-Dec-27	15-Feb-26	28-Dec-26	0%	4,695,555	4,695,555
Tie In To Existing Networks		215	24-Mar-27	06-Dec-27	02-Sep-26	28-Dec-26	0%	0	0
Phase 2 Block "J"		215	24-Mar-27	06-Dec-27	02-Sep-26	28-Dec-26	0%	0	0
Road 09 Local 2 (2278 LM)		178	24-Mar-27	24-Oct-27	17-Oct-26	20-Dec-26	0%	0	0
Storm Drainage Network		7	02-Sep-27	09-Sep-27	13-Dec-26	20-Dec-26	0%	0	0
TIE-SD-R09	TIE IN Existing Network For Storm Drainage Network	7	02-Sep-27	09-Sep-27	13-Dec-26	20-Dec-26	0%	0	0
Sewage Network		12	14-Aug-27	26-Aug-27	09-Nov-26	22-Nov-26	0%	0	0
TIE-SW-R09	TIE IN Existing Network For Sewage Network	12	14-Aug-27	26-Aug-27	09-Nov-26	22-Nov-26	0%	0	0
Potable Water Network		12	05-Oct-27	18-Oct-27	19-Nov-26	02-Dec-26	0%	0	0
TIE-PW-R09	TIE IN Existing Network For Potable Water Network	12	05-Oct-27	18-Oct-27	19-Nov-26	02-Dec-26	0%	0	0
Irrigation Network		12	24-Jul-27	05-Aug-27	29-Oct-26	11-Nov-26	0%	0	0
TIE-IR-R09	TIE IN Existing Network For Irrigation Network	12	24-Jul-27	05-Aug-27	29-Oct-26	11-Nov-26	0%	0	0
Meduim Voltage Network		18	24-Mar-27	13-Apr-27	29-Oct-26	18-Nov-26	0%	0	0
TIE-R09-MV	TIE IN Existing Network For Medium Voltage Network	18	24-Mar-27	13-Apr-27	29-Oct-26	18-Nov-26	0%	0	0
Street Lighting Network		18	04-Oct-27	24-Oct-27	17-Oct-26	05-Nov-26	0%	0	0
TIE-R09-SL	TIE IN Existing Network For Street Lighting Network	18	04-Oct-27	24-Oct-27	17-Oct-26	05-Nov-26	0%	0	0
Telecom Network		10	11-May-27	27-May-27	29-Oct-26	09-Nov-26	0%	0	0
TIE-R09-TE	TIE IN Existing Network For Telecom Network	10	11-May-27	27-May-27	29-Oct-26	09-Nov-26	0%	0	0
Road 10 Local 2 (2352 LM)		215	24-Mar-27	06-Dec-27	17-Oct-26	28-Dec-26	0%	0	0
Storm Drainage Network		7	02-Sep-27	09-Sep-27	13-Dec-26	20-Dec-26	0%	0	0
TIE-SD-R10	TIE IN Existing Network For Storm Drainage Network	7	02-Sep-27	09-Sep-27	13-Dec-26	20-Dec-26	0%	0	0
Sewage Network		12	14-Aug-27	26-Aug-27	09-Nov-26	22-Nov-26	0%	0	0
TIE-SW-R10	TIE IN Existing Network For Sewage Network	12	14-Aug-27	26-Aug-27	09-Nov-26	22-Nov-26	0%	0	0
Potable Water Network		12	05-Oct-27	18-Oct-27	19-Nov-26	02-Dec-26	0%	0	0
TIE-PW-R10	TIE IN Existing Network For Potable Water Network	12	05-Oct-27	18-Oct-27	19-Nov-26	02-Dec-26	0%	0	0
Irrigation Network		12	24-Jul-27	05-Aug-27	29-Oct-26	11-Nov-26	0%	0	0
TIE-IR-R10	TIE IN Existing Network For Irrigation Network	12	24-Jul-27	05-Aug-27	29-Oct-26	11-Nov-26	0%	0	0
Meduim Voltage Network		18	24-Mar-27	13-Apr-27	29-Oct-26	18-Nov-26	0%	0	0
TIE-R10-MV	TIE IN Existing Network For Medium Voltage Network	18	24-Mar-27	13-Apr-27	29-Oct-26	18-Nov-26	0%	0	0
Street Lighting Network		18	04-Oct-27	24-Oct-27	17-Oct-26	05-Nov-26	0%	0	0

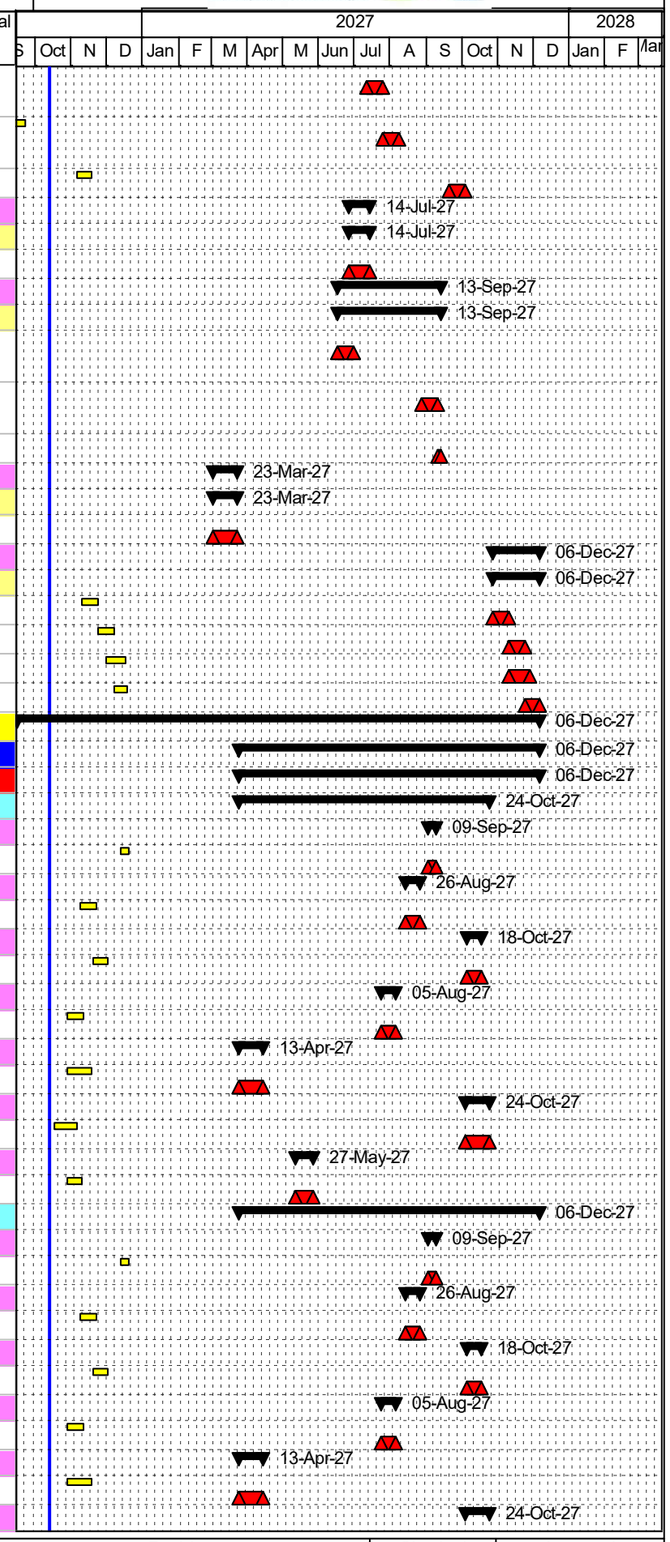

Primary Baseline | Actual Work | Summary
Remaining Work | Baseline Milestone
Critical Remaining Work | Milestone

Date	Revision	Checked	Approved
13-Oct-26	Third Industrial City		


Activity ID	Activity Name	Original Duration	Start	Finish	BL Project Start	BL Project Finish	Performance % Complete	Budgeted Total Cost	Remaining Total Cost
TIE-R10-SL	TIE IN Existing Network For Street Lighting Network	18	04-Oct-27	24-Oct-27	17-Oct-26	05-Nov-26	0%	0	0
Telecom Network		10	11-May-27	27-May-27	29-Oct-26	09-Nov-26	0%	0	0
TIE-R10-TE	TIE IN Existing Network For Telecom Network	10	11-May-27	27-May-27	29-Oct-26	09-Nov-26	0%	0	0
Road Works		5	30-Nov-27	06-Dec-27	23-Dec-26	28-Dec-26	0%	0	0
TIE-R10-RD	TIE IN Existing Network For Road Works	5	30-Nov-27	06-Dec-27	23-Dec-26	28-Dec-26	0%	0	0
Road 11 Local 1 (670 LM)		215	24-Mar-27	06-Dec-27	17-Oct-26	28-Dec-26	0%	0	0
Storm Drainage Network		7	02-Sep-27	09-Sep-27	13-Dec-26	20-Dec-26	0%	0	0
TIE-SD-R11	TIE IN Existing Network For Storm Drainage Network	7	02-Sep-27	09-Sep-27	13-Dec-26	20-Dec-26	0%	0	0
Sewage Network		12	14-Aug-27	26-Aug-27	09-Nov-26	22-Nov-26	0%	0	0
TIE-SW-R11	TIE IN Existing Network For Sewage Network	12	14-Aug-27	26-Aug-27	09-Nov-26	22-Nov-26	0%	0	0
Potable Water Network		12	05-Oct-27	18-Oct-27	19-Nov-26	02-Dec-26	0%	0	0
TIE-PW-R11	TIE IN Existing Network For Potable Water Network	12	05-Oct-27	18-Oct-27	19-Nov-26	02-Dec-26	0%	0	0
Irrigation Network		12	24-Jul-27	05-Aug-27	29-Oct-26	11-Nov-26	0%	0	0
TIE-IR-R11	TIE IN Existing Network For Irrigation Network	12	24-Jul-27	05-Aug-27	29-Oct-26	11-Nov-26	0%	0	0
Meduim Voltage Network		18	24-Mar-27	13-Apr-27	29-Oct-26	18-Nov-26	0%	0	0
TIE-R11-MV	TIE IN Existing Network For Medium Voltage Network	18	24-Mar-27	13-Apr-27	29-Oct-26	18-Nov-26	0%	0	0
Street Lighting Network		18	04-Oct-27	24-Oct-27	17-Oct-26	05-Nov-26	0%	0	0
TIE-R11-SL	TIE IN Existing Network For Street Lighting Network	18	04-Oct-27	24-Oct-27	17-Oct-26	05-Nov-26	0%	0	0
Telecom Network		10	11-May-27	27-May-27	29-Oct-26	09-Nov-26	0%	0	0
TIE-R11-TE	TIE IN Existing Network For Telecom Network	10	11-May-27	27-May-27	29-Oct-26	09-Nov-26	0%	0	0
Road Works		5	30-Nov-27	06-Dec-27	23-Dec-26	28-Dec-26	0%	0	0
TIE-R11-RD	TIE IN Existing Network For Road Works	5	30-Nov-27	06-Dec-27	23-Dec-26	28-Dec-26	0%	0	0
Road 14 Local 1 (584 LM)		215	24-Mar-27	06-Dec-27	17-Oct-26	28-Dec-26	0%	0	0
Storm Drainage Network		7	02-Sep-27	09-Sep-27	13-Dec-26	20-Dec-26	0%	0	0
TIE-SD-R14	TIE IN Existing Network For Storm Drainage Network	7	02-Sep-27	09-Sep-27	13-Dec-26	20-Dec-26	0%	0	0
Sewage Network		12	14-Aug-27	26-Aug-27	09-Nov-26	22-Nov-26	0%	0	0
TIE-SW-R14	TIE IN Existing Network For Sewage Network	12	14-Aug-27	26-Aug-27	09-Nov-26	22-Nov-26	0%	0	0
Potable Water Network		12	05-Oct-27	18-Oct-27	19-Nov-26	02-Dec-26	0%	0	0
TIE-PW-R14	TIE IN Existing Network For Potable Water Network	12	05-Oct-27	18-Oct-27	19-Nov-26	02-Dec-26	0%	0	0
Irrigation Network		12	24-Jul-27	05-Aug-27	29-Oct-26	11-Nov-26	0%	0	0
TIE-IR-R14	TIE IN Existing Network For Irrigation Network	12	24-Jul-27	05-Aug-27	29-Oct-26	11-Nov-26	0%	0	0
Meduim Voltage Network		18	24-Mar-27	13-Apr-27	29-Oct-26	18-Nov-26	0%	0	0
TIE-R14-MV	TIE IN Existing Network For Medium Voltage Network	18	24-Mar-27	13-Apr-27	29-Oct-26	18-Nov-26	0%	0	0
Street Lighting Network		18	04-Oct-27	24-Oct-27	17-Oct-26	05-Nov-26	0%	0	0
TIE-R14-SL	TIE IN Existing Network For Street Lighting Network	18	04-Oct-27	24-Oct-27	17-Oct-26	05-Nov-26	0%	0	0
Telecom Network		10	11-May-27	27-May-27	29-Oct-26	09-Nov-26	0%	0	0
TIE-R14-TE	TIE IN Existing Network For Telecom Network	10	11-May-27	27-May-27	29-Oct-26	09-Nov-26	0%	0	0
Road Works		5	30-Nov-27	06-Dec-27	23-Dec-26	28-Dec-26	0%	0	0
TIE-R14-RD	TIE IN Existing Network For Road Works	5	30-Nov-27	06-Dec-27	23-Dec-26	28-Dec-26	0%	0	0
Road 15 Local 1 (556 LM)		178	24-Mar-27	24-Oct-27	17-Oct-26	20-Dec-26	0%	0	0
Storm Drainage Network		7	02-Sep-27	09-Sep-27	13-Dec-26	20-Dec-26	0%	0	0
TIE-SD-R15	TIE IN Existing Network For Storm Drainage Network	7	02-Sep-27	09-Sep-27	13-Dec-26	20-Dec-26	0%	0	0
Sewage Network		12	14-Aug-27	26-Aug-27	09-Nov-26	22-Nov-26	0%	0	0
TIE-SW-R15	TIE IN Existing Network For Sewage Network	12	14-Aug-27	26-Aug-27	09-Nov-26	22-Nov-26	0%	0	0
Potable Water Network		12	05-Oct-27	18-Oct-27	19-Nov-26	02-Dec-26	0%	0	0
TIE-PW-R15	TIE IN Existing Network For Potable Water Network	12	05-Oct-27	18-Oct-27	19-Nov-26	02-Dec-26	0%	0	0
Irrigation Network		12	24-Jul-27	05-Aug-27	29-Oct-26	11-Nov-26	0%	0	0
TIE-IR-R15	TIE IN Existing Network For Irrigation Network	12	24-Jul-27	05-Aug-27	29-Oct-26	11-Nov-26	0%	0	0
Meduim Voltage Network		18	24-Mar-27	13-Apr-27	29-Oct-26	18-Nov-26	0%	0	0
TIE-R15-MV	TIE IN Existing Network For Medium Voltage Network	18	24-Mar-27	13-Apr-27	29-Oct-26	18-Nov-26	0%	0	0
Street Lighting Network		18	04-Oct-27	24-Oct-27	17-Oct-26	05-Nov-26	0%	0	0
TIE-R15-SL	TIE IN Existing Network For Street Lighting Network	18	04-Oct-27	24-Oct-27	17-Oct-26	05-Nov-26	0%	0	0
Telecom Network		10	11-May-27	27-May-27	29-Oct-26	09-Nov-26	0%	0	0

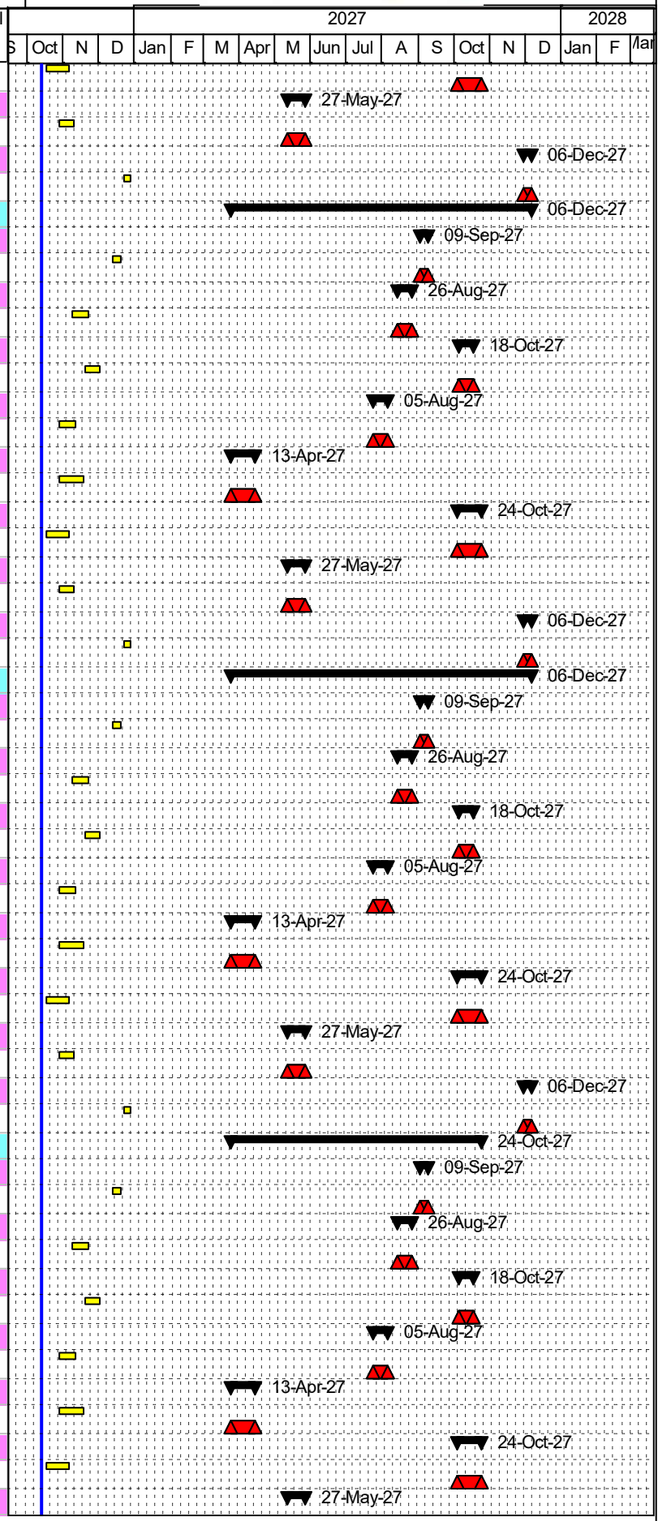

Primary Baseline
Remaining Work
Critical Remaining Work
Actual Work
Baseline Milestone
Milestone
Summary

Date	Revision	Checked	Approved
13-Oct-26	Third Industrial City		


Activity ID	Activity Name	Original Duration	Start	Finish	BL Project Start	BL Project Finish	Performance % Complete	Budgeted Total Cost	Remaining Total Cost
TIE-R15-TE	TIE IN Existing Network For Telecom Network	10	11-May-27	27-May-27	29-Oct-26	09-Nov-26	0%	0	0
Road 16 Local 1 (527 LM)		178	24-Mar-27	24-Oct-27	17-Oct-26	20-Dec-26	0%	0	0
Storm Drainage Network		7	02-Sep-27	09-Sep-27	13-Dec-26	20-Dec-26	0%	0	0
TIE-SD-R16	TIE IN Existing Network For Storm Drainage Network	7	02-Sep-27	09-Sep-27	13-Dec-26	20-Dec-26	0%	0	0
Sewage Network		12	14-Aug-27	26-Aug-27	09-Nov-26	22-Nov-26	0%	0	0
TIE-SW-R16	TIE IN Existing Network For Sewage Network	12	14-Aug-27	26-Aug-27	09-Nov-26	22-Nov-26	0%	0	0
Potable Water Network		12	05-Oct-27	18-Oct-27	19-Nov-26	02-Dec-26	0%	0	0
TIE-PW-R16	TIE IN Existing Network For Potable Water Network	12	05-Oct-27	18-Oct-27	19-Nov-26	02-Dec-26	0%	0	0
Irrigation Network		12	24-Jul-27	05-Aug-27	29-Oct-26	11-Nov-26	0%	0	0
TIE-IR-R16	TIE IN Existing Network For Irrigation Network	12	24-Jul-27	05-Aug-27	29-Oct-26	11-Nov-26	0%	0	0
Meduim Voltage Network		18	24-Mar-27	13-Apr-27	29-Oct-26	18-Nov-26	0%	0	0
TIE-R16-MV	TIE IN Existing Network For Medium Voltage Network	18	24-Mar-27	13-Apr-27	29-Oct-26	18-Nov-26	0%	0	0
Street Lighting Network		18	04-Oct-27	24-Oct-27	17-Oct-26	05-Nov-26	0%	0	0
TIE-R16-SL	TIE IN Existing Network For Street Lighting Network	18	04-Oct-27	24-Oct-27	17-Oct-26	05-Nov-26	0%	0	0
Telecom Network		10	11-May-27	27-May-27	29-Oct-26	09-Nov-26	0%	0	0
TIE-R16-TE	TIE IN Existing Network For Telecom Network	10	11-May-27	27-May-27	29-Oct-26	09-Nov-26	0%	0	0
Road 17 Local 1 (500 LM)		178	24-Mar-27	24-Oct-27	17-Oct-26	20-Dec-26	0%	0	0
Storm Drainage Network		7	02-Sep-27	09-Sep-27	13-Dec-26	20-Dec-26	0%	0	0
TIE-SD-R17	TIE IN Existing Network For Storm Drainage Network	7	02-Sep-27	09-Sep-27	13-Dec-26	20-Dec-26	0%	0	0
Sewage Network		12	14-Aug-27	26-Aug-27	09-Nov-26	22-Nov-26	0%	0	0
TIE-SW-R17	TIE IN Existing Network For Sewage Network	12	14-Aug-27	26-Aug-27	09-Nov-26	22-Nov-26	0%	0	0
Potable Water Network		12	05-Oct-27	18-Oct-27	19-Nov-26	02-Dec-26	0%	0	0
TIE-PW-R17	TIE IN Existing Network For Potable Water Network	12	05-Oct-27	18-Oct-27	19-Nov-26	02-Dec-26	0%	0	0
Irrigation Network		12	24-Jul-27	05-Aug-27	29-Oct-26	11-Nov-26	0%	0	0
TIE-IR-R17	TIE IN Existing Network For Irrigation Network	12	24-Jul-27	05-Aug-27	29-Oct-26	11-Nov-26	0%	0	0
Meduim Voltage Network		18	24-Mar-27	13-Apr-27	29-Oct-26	18-Nov-26	0%	0	0
TIE-R17-MV	TIE IN Existing Network For Medium Voltage Network	18	24-Mar-27	13-Apr-27	29-Oct-26	18-Nov-26	0%	0	0
Street Lighting Network		18	04-Oct-27	24-Oct-27	17-Oct-26	05-Nov-26	0%	0	0
TIE-R17-SL	TIE IN Existing Network For Street Lighting Network	18	04-Oct-27	24-Oct-27	17-Oct-26	05-Nov-26	0%	0	0
Telecom Network		10	11-May-27	27-May-27	29-Oct-26	09-Nov-26	0%	0	0
TIE-R17-TE	TIE IN Existing Network For Telecom Network	10	11-May-27	27-May-27	29-Oct-26	09-Nov-26	0%	0	0
Road 18 Local 1 (479 LM)		178	24-Mar-27	24-Oct-27	02-Sep-26	20-Dec-26	0%	0	0
Storm Drainage Network		7	02-Sep-27	09-Sep-27	13-Dec-26	20-Dec-26	0%	0	0
TIE-SD-R18	TIE IN Existing Network For Storm Drainage Network	7	02-Sep-27	09-Sep-27	13-Dec-26	20-Dec-26	0%	0	0
Sewage Network		12	14-Aug-27	26-Aug-27	09-Nov-26	22-Nov-26	0%	0	0
TIE-SW-R18	TIE IN Existing Network For Sewage Network	12	14-Aug-27	26-Aug-27	09-Nov-26	22-Nov-26	0%	0	0
Potable Water Network		12	05-Oct-27	18-Oct-27	19-Nov-26	02-Dec-26	0%	0	0
TIE-PW-R18	TIE IN Existing Network For Potable Water Network	12	05-Oct-27	18-Oct-27	19-Nov-26	02-Dec-26	0%	0	0
Irrigation Network		12	24-Jul-27	05-Aug-27	29-Oct-26	11-Nov-26	0%	0	0
TIE-IR-R18	TIE IN Existing Network For Irrigation Network	12	24-Jul-27	05-Aug-27	29-Oct-26	11-Nov-26	0%	0	0
Meduim Voltage Network		18	24-Mar-27	13-Apr-27	29-Oct-26	18-Nov-26	0%	0	0
TIE-R18-MV10	TIE IN Existing Network For Medium Voltage Network	18	24-Mar-27	13-Apr-27	29-Oct-26	18-Nov-26	0%	0	0
Street Lighting Network		18	04-Oct-27	24-Oct-27	17-Oct-26	05-Nov-26	0%	0	0
TIE-R18-SL10	TIE IN Existing Network For Street Lighting Network	18	04-Oct-27	24-Oct-27	17-Oct-26	05-Nov-26	0%	0	0
Telecom Network		12	11-May-27	30-May-27	02-Sep-26	15-Sep-26	0%	0	0
TIE-R18-TE10	TIE IN Existing Network For Telecom Network	12	11-May-27	30-May-27	02-Sep-26	15-Sep-26	0%	0	0
Sewage Pump Stations		361	16-Sep-26 A	15-Jun-27	05-Apr-26	01-Dec-26	0%	4,380,241	4,380,241
Sewage Pump Station (PS 06)		361	16-Sep-26 A	15-Jun-27	05-Apr-26	01-Dec-26	0%	4,380,241	4,380,241
Pump Station Main Building		309	16-Sep-26 A	10-Apr-27	05-Apr-26	06-Oct-26	0%	1,517,233	1,517,233
CO-SW-PS7-MB-11(	Concrete Works of Superstrucure	30	16-Sep-26 A	16-Nov-26	05-Apr-26	09-May-26	0%	66,973	66,973
CO-SW-PS7-MB-12(	Internal Finishes Works of Superstrucure	30	17-Nov-26	21-Dec-26	10-May-26	17-Jun-26	0%	19,135	19,135
CO-SW-PS7-MB-13(	Internal Electrical Works	30	22-Dec-26	25-Jan-27	18-Jun-26	22-Jul-26	0%	697,563	697,563
CO-SW-PS7-MB-14(	Internal Mechanical Works	30	26-Jan-27	02-Mar-27	23-Jul-26	26-Aug-26	0%	572,621	572,621

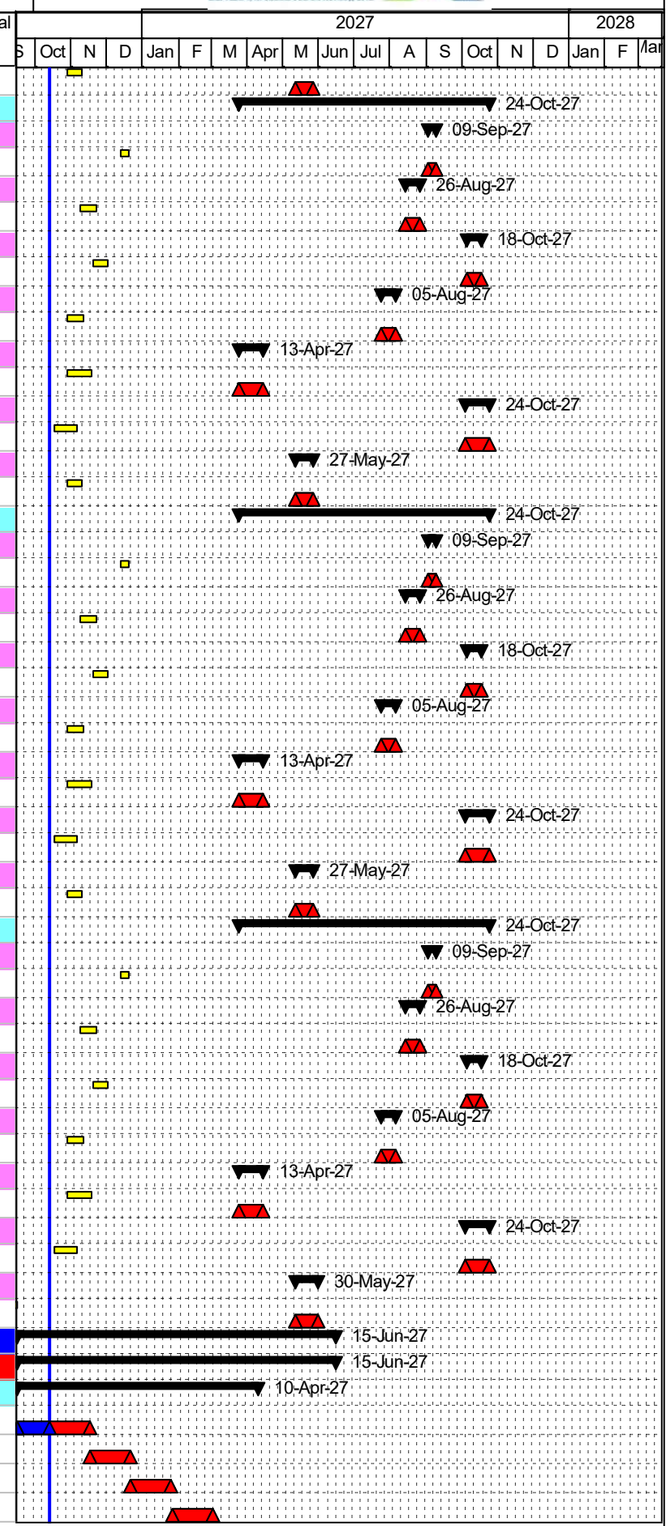

Primary Baseline | Actual Work | Summary
Remaining Work | Baseline Milestone
Critical Remaining Work | Milestone

Date	Revision	Checked	Approved
13-Oct-26	Third Industrial City		

Activity ID	Activity Name	Original Duration	Start	Finish	BL Project Start	BL Project Finish	Performance % Complete	Budgeted Total Cost	Remaining Total Cost
CO-SW-PS7-MB-15(	Electromechanical Main Works	30	03-Mar-27	10-Apr-27	01-Sep-26	06-Oct-26	0%	160,941	160,941
Generator With Umbrella Tank		75	22-Dec-26	23-Mar-27	18-Jun-26	13-Sep-26	0%	215,257	215,257
CO-SW-PS7-GN-10(	Concrete Works of Base	12	22-Dec-26	04-Jan-27	18-Jun-26	01-Jul-26	0%	43,051	43,051
CO-SW-PS7-GN-11(	Install Manually Operated Fuel Pump	21	05-Jan-27	28-Jan-27	02-Jul-26	26-Jul-26	0%	107,628	107,628
CO-SW-PS7-GN-12(	Install Ground Fuel Tank	21	30-Jan-27	23-Feb-27	27-Jul-26	19-Aug-26	0%	43,051	43,051
CO-SW-PS7-GN-13(	Fix Steel Structure for Umbrella	21	24-Feb-27	23-Mar-27	20-Aug-26	13-Sep-26	0%	21,526	21,526
Motor Control Centre Building		121	17-Nov-26	11-Apr-27	10-May-26	03-Oct-26	0%	1,971,445	1,971,445
CO-SW-PS7-MCC-1	Excavation Main Bulding	16	17-Nov-26	05-Dec-26	10-May-26	01-Jun-26	0%	96	96
CO-SW-PS7-MCC-1	Concrete Works of Superstrucure	21	06-Dec-26	29-Dec-26	02-Jun-26	25-Jun-26	0%	108,090	108,090
CO-SW-PS7-MCC-1	Internal Finishes Works of Superstrucure	21	30-Dec-26	23-Jan-27	27-Jun-26	20-Jul-26	0%	65,710	65,710
CO-SW-PS7-MCC-1	Internal Electrical Works	21	24-Jan-27	16-Feb-27	21-Jul-26	13-Aug-26	0%	298,746	298,746
CO-SW-PS7-MCC-1	Internal Mechanical Works	21	17-Feb-27	17-Mar-27	15-Aug-26	07-Sep-26	0%	75,272	75,272
CO-SW-PS7-MCC-1	Electromechanical Main Works	21	18-Mar-27	11-Apr-27	08-Sep-26	03-Oct-26	0%	1,423,530	1,423,530
Simple Building Works		50	24-Mar-27	26-May-27	14-Sep-26	11-Nov-26	0%	468,576	468,576
CO-SW-PS7-SBL-10	Perimeter Fencing	23	24-Mar-27	19-Apr-27	14-Sep-26	11-Oct-26	0%	73,149	73,149
CO-SW-PS7-SBL-11	Outside Lighting	27	20-Apr-27	26-May-27	12-Oct-26	11-Nov-26	0%	16,426	16,426
CO-SW-PS7-SBL-12	Outside Duct Works	23	20-Apr-27	22-May-27	12-Oct-26	07-Nov-26	0%	9,923	9,923
CO-SW-PS7-SBL-13	Rectangular Wet Wells	27	20-Apr-27	26-May-27	12-Oct-26	11-Nov-26	0%	147,819	147,819
CO-SW-PS7-SBL-14	Round Wet Well Structure for basket screen	27	20-Apr-27	26-May-27	12-Oct-26	11-Nov-26	0%	67,771	67,771
CO-SW-PS7-SBL-15	Motorized basket screen	27	20-Apr-27	26-May-27	12-Oct-26	11-Nov-26	0%	153,488	153,488
Site Work and Service Road		21	23-May-27	15-Jun-27	08-Nov-26	01-Dec-26	0%	207,730	207,730
CO-SW-PS7-SWS-1	Outside Strom Drainage System	6	23-May-27	29-May-27	08-Nov-26	14-Nov-26	0%	40,230	40,230
CO-SW-PS7-SWS-1	Bituminous Works	15	30-May-27	15-Jun-27	15-Nov-26	01-Dec-26	0%	167,500	167,500
Storm Drainage Ponds		243	13-Oct-26	02-Aug-27	15-Feb-26	24-Aug-26	0%	315,314	315,314
Storm Drainage Pond (PO-J1)		136	13-Oct-26	24-Mar-27	15-Feb-26	30-Jul-26	0%	28,703	28,703
CO-SD-PO-K1-110-P	Finished Grouted Riprap - PART 1	21	13-Oct-26	05-Nov-26	15-Feb-26	10-Mar-26	0%	5,741	5,741
CO-SD-PO-K1-110-P	Finished Grouted Riprap - PART 2	21	07-Nov-26	30-Nov-26	11-Mar-26	07-Apr-26	0%	5,741	5,741
CO-SD-PO-K1-110-P	Finished Grouted Riprap - PART 3	21	01-Dec-26	24-Dec-26	08-Apr-26	02-May-26	0%	5,741	5,741
CO-SD-PO-K1-110-P	Finished Grouted Riprap - PART 4	21	26-Dec-26	18-Jan-27	03-May-26	31-May-26	0%	5,741	5,741
CO-SD-PO-K1-120	Outfall structure	26	19-Jan-27	17-Feb-27	01-Jun-26	30-Jun-26	0%	2,870	2,870
CO-SD-PO-K1-130	Acess Entrace Ramp	26	18-Feb-27	24-Mar-27	01-Jul-26	30-Jul-26	0%	2,870	2,870
Storm Drainage Pond (PO-J2)		157	21-Jan-27	02-Aug-27	15-Feb-26	24-Aug-26	0%	286,611	286,611
CO-SD-PO-K2-100-P	Excavation & Filling Works - PART 1	21	21-Jan-27	14-Feb-27	15-Feb-26	10-Mar-26	0%	68,424	68,424
CO-SD-PO-K2-110-P	Finished Grouted Riprap - PART 1	21	15-Feb-27	15-Mar-27	11-Mar-26	07-Apr-26	0%	2,583	2,583
CO-SD-PO-K2-100-P	Excavation & Filling Works - PART 2	21	15-Feb-27	15-Mar-27	11-Mar-26	07-Apr-26	0%	68,424	68,424
CO-SD-PO-K2-110-P	Finished Grouted Riprap - PART 2	21	16-Mar-27	08-Apr-27	08-Apr-26	02-May-26	0%	2,583	2,583
CO-SD-PO-K2-100-P	Excavation & Filling Works - PART 3	21	16-Mar-27	08-Apr-27	08-Apr-26	02-May-26	0%	68,424	68,424
CO-SD-PO-K2-110-P	Finished Grouted Riprap - PART 3	21	10-Apr-27	03-May-27	03-May-26	31-May-26	0%	2,583	2,583
CO-SD-PO-K2-100-P	Excavation & Filling Works - PART 4	21	10-Apr-27	03-May-27	03-May-26	31-May-26	0%	68,424	68,424
CO-SD-PO-K2-110-P	Finished Grouted Riprap - PART 4	21	04-May-27	02-Jun-27	01-Jun-26	24-Jun-26	0%	2,583	2,583
CO-SD-PO-K2-120	Outfall structure	26	03-Jun-27	03-Jul-27	25-Jun-26	25-Jul-26	0%	1,292	1,292
CO-SD-PO-K2-130	Acess Entrace Ramp	26	04-Jul-27	02-Aug-27	26-Jul-26	24-Aug-26	0%	1,292	1,292
Testing and Comissioning		278	01-Jun-26 A	06-Dec-27	25-Aug-26	03-Jan-27	64.59%	11,395,586	11,395,586
Infrastructure Networks		50	01-Jun-26 A	06-Dec-27	07-Nov-26	03-Jan-27	66.45%	11,075,669	11,075,669
Irrigation Network		12	05-Jun-26 A	05-Aug-27	12-Nov-26	25-Nov-26	25%	624,274	624,274
T/C-IR	Testing and Commissioning of Irrigation Network	12	05-Jun-26 A	05-Aug-27	12-Nov-26	25-Nov-26	25%	624,274	624,274
Potable Water Network		12	01-Jul-26 A	18-Oct-27	03-Dec-26	16-Dec-26	60%	1,022,094	1,022,094
T/C-PW	Testing and Commissioning of Potable Water Network	12	01-Jul-26 A	18-Oct-27	03-Dec-26	16-Dec-26	60%	1,022,094	1,022,094
Sewage Network		12	01-Jun-26 A	07-Oct-27	19-Dec-26	31-Dec-26	85%	2,308,897	2,308,897
T/C-SW	Testing and Commissioning of Sewage Network	12	01-Jun-26 A	07-Oct-27	19-Dec-26	31-Dec-26	85%	2,308,897	2,308,897
Storm Drainage Network		10	10-Jun-26 A	09-Sep-27	21-Dec-26	31-Dec-26	85%	2,866,651	2,866,651

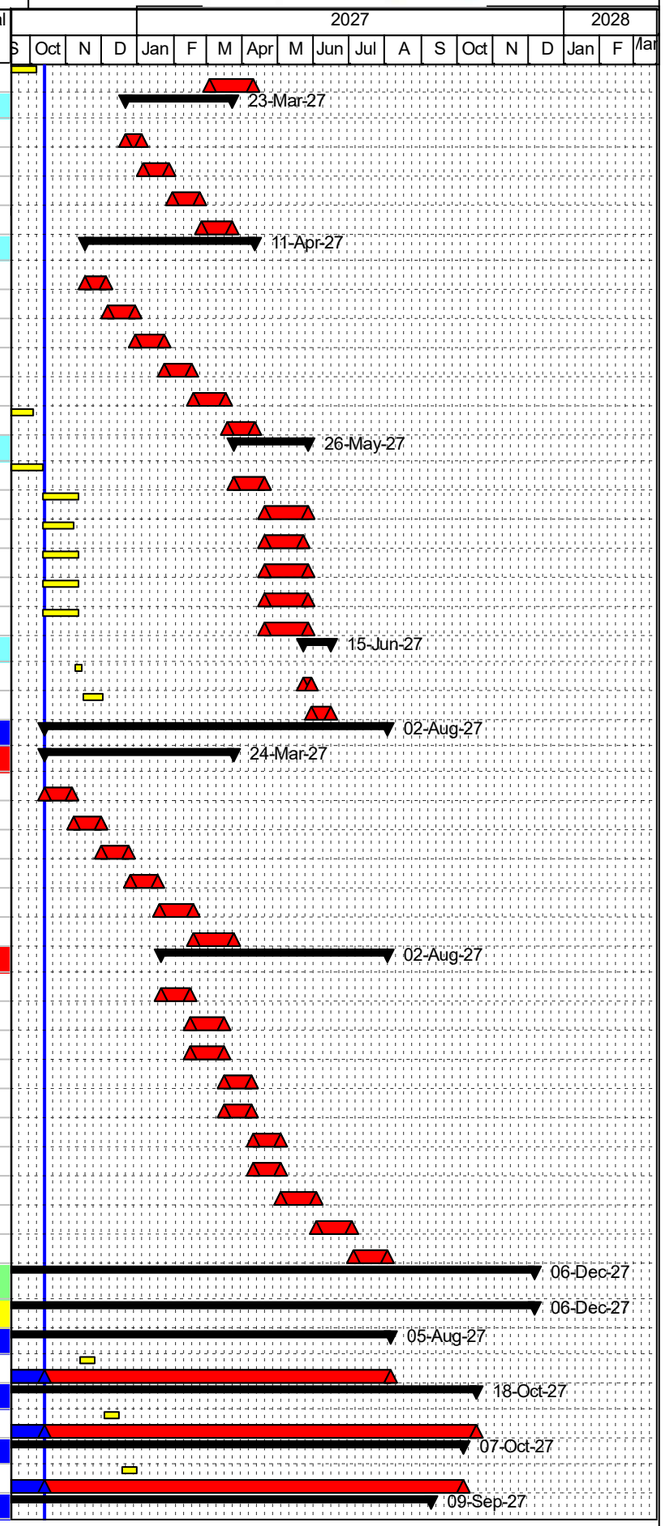


Primary Baseline
Remaining Work
Critical Remaining Work
Actual Work
Baseline Milestone
Milestone
Summary

Date	Revision	Checked	Approved
13-Oct-26	Third Industrial City		

Infrastructure Works of Area J -3rd Industrial City-
Dammam-Phase 2 - Update 13-10-2026
Remaining work

Activity ID	Activity Name	Original Duration	Start	Finish	BL Project Start	BL Project Finish	Performance % Complete	Budgeted Total Cost	Remaining Total Cost
T/C-SD	Testing and Commissioning of Storm Drainage Network	10	10-Jun-26 A	09-Sep-27	21-Dec-26	31-Dec-26	85%	2,866,651	2,866,651
Street Lighting Network		18	05-Sep-26 A	24-Oct-27	07-Nov-26	26-Nov-26	32%	462,378	462,378
T/C-SL	Testing and Commissioning of Street Lighting Network	18	05-Sep-26 A	24-Oct-27	07-Nov-26	26-Nov-26	32%	462,378	462,378
Telecom Network		10	05-Sep-26 A	06-Sep-27	10-Nov-26	21-Nov-26	32%	181,657	181,657
T/C-TE	Testing and Commissioning of Telecom Network	10	05-Sep-26 A	06-Sep-27	10-Nov-26	21-Nov-26	32%	181,657	181,657
Medium Voltage Network		10	05-Sep-26 A	06-Sep-27	22-Nov-26	02-Dec-26	55%	478,905	478,905
T/C-MV	Testing and Commissioning of Medium Voltage Network	10	05-Sep-26 A	06-Sep-27	22-Nov-26	02-Dec-26	55%	478,905	478,905
Road Works		5	16-Aug-26 A	06-Dec-27	29-Dec-26	03-Jan-27	55%	3,130,812	3,130,812
T/C-RD	Testing and Commissioning of Road Works	5	16-Aug-26 A	06-Dec-27	29-Dec-26	03-Jan-27	55%	3,130,812	3,130,812
Independent Works		56	03-Aug-27	07-Oct-27	25-Aug-26	31-Dec-26	0%	319,918	319,918
T/C-DPO	Testing and Commissioning of Storm Drainage Ponds	30	03-Aug-27	06-Sep-27	25-Aug-26	29-Sep-26	0%	296,837	296,837
T/C-SPS	Testing and Commissioning of Sewage Pump Stations	26	07-Sep-27	07-Oct-27	02-Dec-26	31-Dec-26	0%	23,081	23,081
Handing over and close out		160	16-Jun-27	20-Dec-27	17-Oct-26	11-Jan-27	0%	0	0
As-Built		155	16-Jun-27	14-Dec-27	17-Oct-26	05-Jan-27	0%	0	0
HO-210	Submission As-Built Drawing For Pump station	12	16-Jun-27	29-Jun-27	02-Dec-26	15-Dec-26	0%	0	0
HO-180	Submission As-Built Drawing For Irrigation Network	12	24-Jul-27	05-Aug-27	29-Oct-26	11-Nov-26	0%	0	0
HO-130	Submission As-Built Drawing For Pond	12	07-Aug-27	19-Aug-27	12-Nov-26	25-Nov-26	0%	0	0
HO-160	Submission As-Built Drawing For Telecom Network	12	07-Aug-27	19-Aug-27	12-Nov-26	25-Nov-26	0%	0	0
HO-170	Submission As-Built Drawing For Medium Voltage Network	12	07-Aug-27	19-Aug-27	12-Nov-26	25-Nov-26	0%	0	0
HO-200	Submission As-Built Drawing For Storm Network	12	02-Sep-27	15-Sep-27	13-Dec-26	26-Dec-26	0%	0	0
HO-150	Submission As-Built Drawing For Street Lighting Network	12	04-Oct-27	17-Oct-27	17-Oct-26	29-Oct-26	0%	0	0
HO-190	As-Built Drawing For Potable Water Network	12	05-Oct-27	18-Oct-27	19-Nov-26	02-Dec-26	0%	0	0
HO-100	Submission As-Built Drawing For Sewage Network	7	06-Dec-27	14-Dec-27	29-Dec-26	05-Jan-27	0%	0	0
HO-140	Submission As-Built Drawing For Roads Network	5	06-Dec-27	12-Dec-27	29-Dec-26	03-Jan-27	0%	0	0
De-Mobilization Works		5	08-Dec-27	14-Dec-27	04-Jan-27	09-Jan-27	0%	0	0
HO-120	Remove material stock & Storage area	5	08-Dec-27	14-Dec-27	04-Jan-27	09-Jan-27	0%	0	0
HO-220	Removing Portable Caravan	5	08-Dec-27	14-Dec-27	04-Jan-27	09-Jan-27	0%	0	0
HO-230	Remove Temporary Car Shades	5	08-Dec-27	14-Dec-27	04-Jan-27	09-Jan-27	0%	0	0
Handing Over		10	08-Dec-27	20-Dec-27	04-Jan-27	11-Jan-27	0%	0	0
HO-110	Final Testing Work	5	08-Dec-27	14-Dec-27	04-Jan-27	09-Jan-27	0%	0	0
HO-250	Review B.O.Q Qty. to ensure compliance with the actual status	5	12-Dec-27	18-Dec-27	04-Jan-27	09-Jan-27	0%	0	0
HO-260	Review FIR Approval to ensure compliance with the actual status	5	12-Dec-27	18-Dec-27	04-Jan-27	09-Jan-27	0%	0	0
HO-270	Review the sample drawing to ensure compliance with the actual status	5	12-Dec-27	18-Dec-27	04-Jan-27	09-Jan-27	0%	0	0
HO-240	Final Walkthrough and Inspection	2	18-Dec-27	20-Dec-27	10-Jan-27	11-Jan-27	0%	0	0
HO-280	Punch List Completion	2	18-Dec-27	20-Dec-27	10-Jan-27	11-Jan-27	0%	0	0

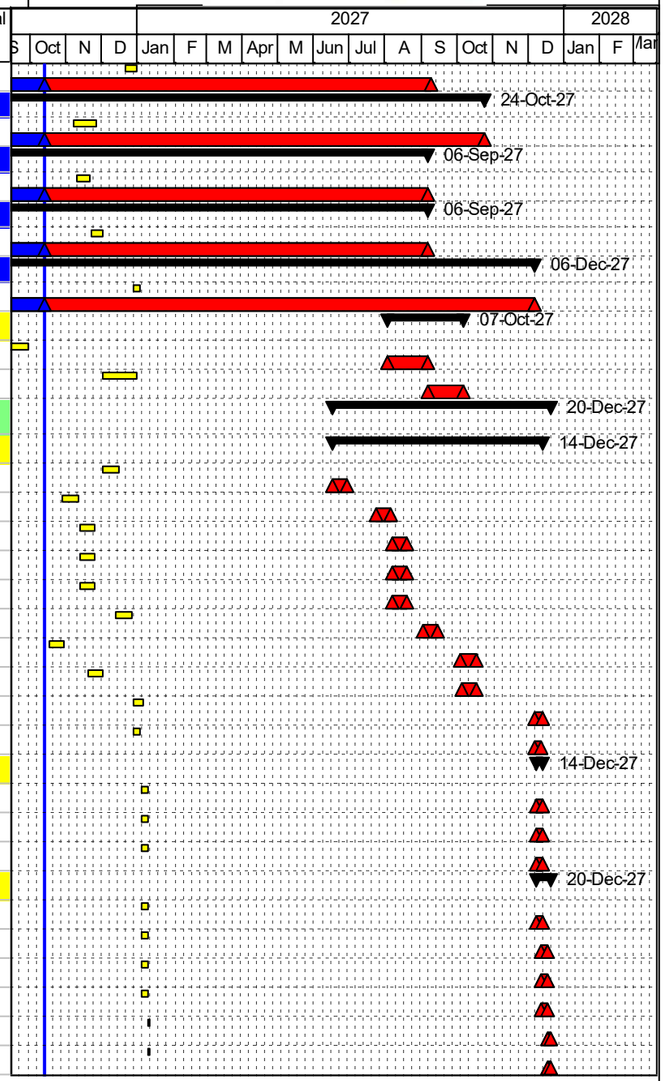

Primary Baseline | Actual Work | Summary
Remaining Work | Baseline Milestone
Critical Remaining Work | Milestone

Date	Revision	Checked	Approved
13-Oct-26	Third Industrial City		
