ENJAZCO


JDH1-02-003 - Infrastructure Development For Industrial City 1 In Jeddah - Update - 06.10.2026

Progress Certificate # 01

egis

MODON

Activity ID	Activity Name	Original Duration	BL Project Start	BL Project Finish	Start	Finish	Performance % Complete	Performance % Complete - Labor Units	Budget At Completion
JDH1.02.003-Up-06.10.2026	JDH1-02-003 - Infrastructure Development For Industı	751	19-Nov-25	18-Nov-27	19-Nov-25 A	06-May-28	77.64%	72.13%	86,756,415.73
JDH1.02.003-Up-06.10.2026.5	Milestones	751	19-Nov-25	18-Nov-27	19-Nov-25 A	06-May-28	0%	0%	0.00
JDH1.02.003-Up-06.10.2026.5.1	Key Milestones	751	19-Nov-25	18-Nov-27	19-Nov-25 A	06-May-28	0%	0%	0.00
JDH1.02.003-Up-06.10.2026.5.2	Contractual Milestone	721	18-Dec-25	18-Nov-27	18-Dec-25 A	06-May-28	0%	0%	0.00
JDH1.02.003-Up-06.10.2026.5.6	Monitoring and Control Milestone	260	04-May-27	18-Oct-27	06-Jun-27	04-Apr-28	0%	0%	0.00
JDH1.02.003-Up-06.10.2026.2	Mobilization	112	19-Nov-25	18-Dec-25	19-Nov-25 A	04-Mar-26 A	0%	100%	0.00
JDH1.02.003-Up-06.10.2026.2.4	Topographic Survey	8	19-Nov-25	27-Nov-25	19-Nov-25 A	27-Nov-25 A	0%	100%	0.00
JDH1.02.003-Up-06.10.2026.2.2	Site Facilities & Offices	44	19-Nov-25	18-Dec-25	19-Nov-25 A	12-Jan-26 A	0%	100%	0.00
JDH1.02.003-Up-06.10.2026.2.1	Permit's and Authority Approvals	47	19-Nov-25	09-Dec-25	19-Nov-25 A	20-Nov-25 A	0%	100%	0.00
JDH1.02.003-Up-06.10.2026.2.3	Preliminary Submittals	112	19-Nov-25	18-Dec-25	19-Nov-25 A	04-Mar-26 A	0%	100%	0.00
JDH1.02.003-Up-06.10.2026.3	Engineering	275	26-Nov-25	19-Jan-26	01-Dec-25 A	24-Oct-26	99.14%	98.79%	2,601,460.39
JDH1.02.003-Up-06.10.2026.3.2	Shop Drawings	264	29-Nov-25	19-Jan-26	04-Dec-25 A	24-Oct-26	0%	97.7%	0.00
JDH1.02.003-Up-06.10.2026.3.3	Method Statements	83	26-Nov-25	19-Jan-26	10-Dec-25 A	08-Feb-26 A	0%	100%	0.00
JDH1.02.003-Up-06.10.2026.3.4	Pre-qualification and Material	90	15-Dec-25	19-Jan-26	01-Dec-25 A	12-Oct-26	99.14%	99.11%	2,601,460.39
JDH1.02.003-Up-06.10.2026.4	Procurement	514	28-Dec-25	14-Sep-27	25-Nov-25 A	07-Sep-27	89.19%	82.42%	17,355,662.10
JDH1.02.003-Up-06.10.2026.4.2	Short Lead Item	488	28-Dec-25	06-Apr-27	25-Nov-25 A	09-Aug-27	93.34%	85.43%	6,936,333.10
JDH1.02.003-Up-06.10.2026.4.1	Long Lead Item	509	30-Dec-25	14-Sep-27	09-Dec-25 A	07-Sep-27	86.43%	82.23%	10,419,329.00
JDH1.02.003-Up-06.10.2026.1	Construction	698	20-Dec-25	18-Oct-27	20-Nov-25 A	04-Apr-28	75.59%	70.43%	58,121,602.04
JDH1.02.003-Up-06.10.2026.1.9	Site Demolition	93	20-Dec-25	03-Mar-26	20-Nov-25 A	02-Feb-26 A	100%	100%	279,942.75
JDH1.02.003-Up-06.10.2026.1.1	Roads & Meduim Voltage	411	06-Jan-26	17-Sep-26	01-Dec-25 A	05-Jun-27	73.25%	73.46%	11,810,038.74
JDH1.02.003-Up-06.10.2026.1.6	Deep Infrastructure network	265	01-Apr-26	18-Nov-26	27-Dec-25 A	04-Jan-27	97.3%	95.92%	10,009,830.20
JDH1.02.003-Up-06.10.2026.1.7	Shallow infrastructure network	421	15-Jun-26	18-Mar-27	13-Jan-26 A	18-Sep-27	82.06%	76.24%	12,539,076.30
JDH1.02.003-Up-06.10.2026.1.3	Bridge	443	04-Mar-26	01-Jun-27	17-Jan-26 A	15-Aug-27	72.83%	87.06%	2,513,306.98
JDH1.02.003-Up-06.10.2026.1.4	Outside Boundary Area (Tie-in Lines)	419	01-Jan-26	04-May-27	05-Jan-26 A	06-Jun-27	99.31%	99.68%	2,681,726.27
JDH1.02.003-Up-06.10.2026.1.8	Roads Finishing	192	25-Jan-27	03-Aug-27	06-May-26 A	24-Nov-27	63.03%	63.79%	8,138,565.00
JDH1.02.003-Up-06.10.2026.1.5	Fence and Gate	549	07-Feb-26	18-Oct-27	10-Dec-25 A	20-Nov-27	65.81%	57.96%	8,127,691.90
JDH1.02.003-Up-06.10.2026.1.2	Roundabout & Landscape	224	14-Mar-27	18-Oct-27	18-Jul-27	04-Apr-28	0%	0%	2,021,423.90
JDH1.02.003-Up-06.10.2026.6	Testing & Commissioning	155	04-Aug-27	26-Oct-27	15-Jun-26 A	12-Apr-28	61.84%	51.93%	8,677,691.20
JDH1.02.003-Up-06.10.2026.7	Project Close-out	142	14-Aug-27	18-Nov-27	23-Nov-27	06-May-28	0%	0%	0.00
JDH1.02.003-Up-06.10.2026.7.1	As-Built DWGs	132	14-Aug-27	07-Nov-27	23-Nov-27	24-Apr-28	0%	0%	0.00
JDH1.02.003-Up-06.10.2026.7.2	Demobilization	10	08-Nov-27	18-Nov-27	25-Apr-28	06-May-28	0%	0%	0.00

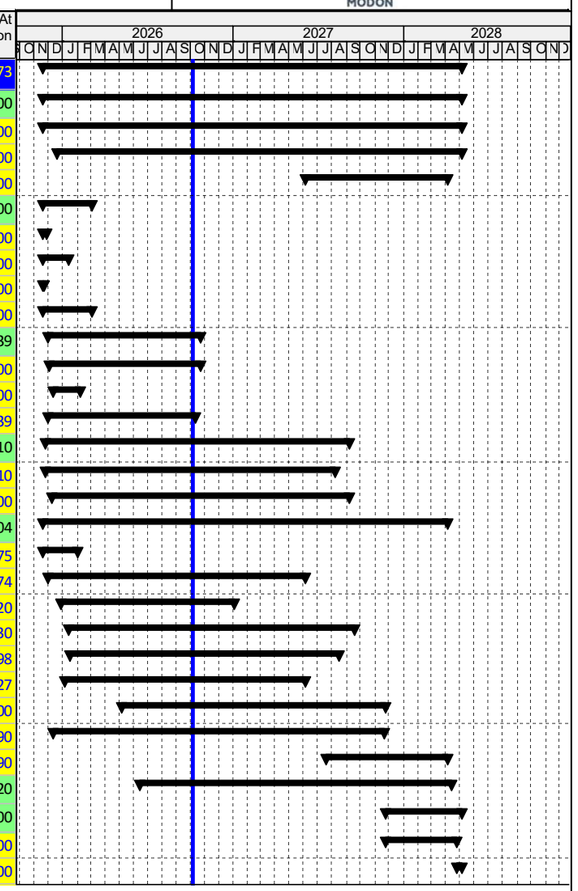

◆ Milestone
summary

TASK filter: All Activities

© Oracle Corporation

06-Oct-26 10:35
