ENJAZCO


# JDH1-02-003 - Infrastructure Development For Industrial City 1 In Jeddah - Update - 20.10.2026

## Progress Certificate # 01

egis

MODON

| Activity ID | Activity Name | Original Duration | BL Project Start | BL Project Finish | Start | Finish | Performance % Complete | Performance % Complete - Labor Units | Budget At Completion |
|---|---|---|---|---|---|---|---|---|---|
| JDH1.02.003-Up-20.10.2026 | JDH1-02-003 - Infrastructure Development For Industri | 763 | 19-Nov-25 | 18-Nov-27 | 19-Nov-25 A | 20-May-28 | 78.74% | 74.06% | 86,756,415.73 |
| JDH1.02.003-Up-20.10.2026.5 | Milestones | 763 | 19-Nov-25 | 18-Nov-27 | 19-Nov-25 A | 20-May-28 | 0% | 0% | 0.00 |
| JDH1.02.003-Up-20.10.2026.5.1 | Key Milestones | 763 | 19-Nov-25 | 18-Nov-27 | 19-Nov-25 A | 20-May-28 | 0% | 0% | 0.00 |
| JDH1.02.003-Up-20.10.2026.5.2 | Contractual Milestone | 733 | 18-Dec-25 | 18-Nov-27 | 18-Dec-25 A | 20-May-28 | 0% | 0% | 0.00 |
| JDH1.02.003-Up-20.10.2026.5.6 | Monitoring and Control Milestone | 260 | 04-May-27 | 18-Oct-27 | 20-Jun-27 | 18-Apr-28 | 0% | 0% | 0.00 |
| JDH1.02.003-Up-20.10.2026.2 | Mobilization | 112 | 19-Nov-25 | 18-Dec-25 | 19-Nov-25 A | 04-Mar-26 A | 0% | 100% | 0.00 |
| JDH1.02.003-Up-20.10.2026.2.4 | Topographic Survey | 8 | 19-Nov-25 | 27-Nov-25 | 19-Nov-25 A | 27-Nov-25 A | 0% | 100% | 0.00 |
| JDH1.02.003-Up-20.10.2026.2.2 | Site Facilities & Offices | 44 | 19-Nov-25 | 18-Dec-25 | 19-Nov-25 A | 12-Jan-26 A | 0% | 100% | 0.00 |
| JDH1.02.003-Up-20.10.2026.2.1 | Permit's and Authority Approvals | 47 | 19-Nov-25 | 09-Dec-25 | 19-Nov-25 A | 20-Nov-25 A | 0% | 100% | 0.00 |
| JDH1.02.003-Up-20.10.2026.2.3 | Preliminary Submittals | 112 | 19-Nov-25 | 18-Dec-25 | 19-Nov-25 A | 04-Mar-26 A | 0% | 100% | 0.00 |
| JDH1.02.003-Up-20.10.2026.3 | Engineering | 287 | 26-Nov-25 | 19-Jan-26 | 01-Dec-25 A | 07-Nov-26 | 99.14% | 98.79% | 2,601,460.39 |
| JDH1.02.003-Up-20.10.2026.3.2 | Shop Drawings | 276 | 29-Nov-25 | 19-Jan-26 | 04-Dec-25 A | 07-Nov-26 | 0% | 97.7% | 0.00 |
| JDH1.02.003-Up-20.10.2026.3.3 | Method Statements | 83 | 26-Nov-25 | 19-Jan-26 | 10-Dec-25 A | 08-Feb-26 A | 0% | 100% | 0.00 |
| JDH1.02.003-Up-20.10.2026.3.4 | Pre-qualification and Material | 90 | 15-Dec-25 | 19-Jan-26 | 01-Dec-25 A | 26-Oct-26 | 99.14% | 99.11% | 2,601,460.39 |
| JDH1.02.003-Up-20.10.2026.4 | Procurement | 502 | 28-Dec-25 | 14-Sep-27 | 25-Nov-25 A | 21-Aug-27 | 90.68% | 91% | 17,355,662.10 |
| JDH1.02.003-Up-20.10.2026.4.2 | Short Lead Item | 498 | 28-Dec-25 | 06-Apr-27 | 25-Nov-25 A | 21-Aug-27 | 94.06% | 86.02% | 6,936,333.10 |
| JDH1.02.003-Up-20.10.2026.4.1 | Long Lead Item | 498 | 30-Dec-25 | 14-Sep-27 | 09-Dec-25 A | 12-Jun-27 | 88.43% | 91.31% | 10,419,329.00 |
| JDH1.02.003-Up-20.10.2026.1 | Construction | 710 | 20-Dec-25 | 18-Oct-27 | 20-Nov-25 A | 18-Apr-28 | 76.69% | 71.61% | 58,121,602.04 |
| JDH1.02.003-Up-20.10.2026.1.9 | Site Demolition | 93 | 20-Dec-25 | 03-Mar-26 | 20-Nov-25 A | 02-Feb-26 A | 100% | 100% | 279,942.75 |
| JDH1.02.003-Up-20.10.2026.1.1 | Roads & Meduim Voltage | 423 | 06-Jan-26 | 17-Sep-26 | 01-Dec-25 A | 19-Jun-27 | 73.25% | 73.46% | 11,810,038.74 |
| JDH1.02.003-Up-20.10.2026.1.6 | Deep Infrastructure network | 277 | 01-Apr-26 | 18-Nov-26 | 27-Dec-25 A | 18-Jan-27 | 97.41% | 95.92% | 10,009,830.20 |
| JDH1.02.003-Up-20.10.2026.1.7 | Shallow infrastructure network | 433 | 15-Jun-26 | 18-Mar-27 | 13-Jan-26 A | 03-Oct-27 | 83.37% | 77.92% | 12,539,076.30 |
| JDH1.02.003-Up-20.10.2026.1.3 | Bridge | 452 | 04-Mar-26 | 01-Jun-27 | 17-Jan-26 A | 25-Aug-27 | 72.83% | 87.06% | 2,513,306.98 |
| JDH1.02.003-Up-20.10.2026.1.4 | Outside Boundary Area (Tie-in Lines) | 419 | 01-Jan-26 | 04-May-27 | 05-Jan-26 A | 20-Jun-27 | 99.31% | 99.68% | 2,681,726.27 |
| JDH1.02.003-Up-20.10.2026.1.8 | Roads Finishing | 204 | 25-Jan-27 | 03-Aug-27 | 06-May-26 A | 08-Dec-27 | 68.7% | 68.4% | 8,138,565.00 |
| JDH1.02.003-Up-20.10.2026.1.5 | Fence and Gate | 558 | 07-Feb-26 | 18-Oct-27 | 10-Dec-25 A | 30-Nov-27 | 65.85% | 58.17% | 8,127,691.90 |
| JDH1.02.003-Up-20.10.2026.1.2 | Roundabout & Landscape | 226 | 14-Mar-27 | 18-Oct-27 | 29-Jul-27 | 18-Apr-28 | 0% | 0% | 2,021,423.90 |
| JDH1.02.003-Up-20.10.2026.6 | Testing & Commissioning | 167 | 04-Aug-27 | 26-Oct-27 | 15-Jun-26 A | 26-Apr-28 | 62.53% | 53.1% | 8,677,691.20 |
| JDH1.02.003-Up-20.10.2026.7 | Project Close-out | 145 | 14-Aug-27 | 18-Nov-27 | 04-Dec-27 | 20-May-28 | 0% | 0% | 0.00 |
| JDH1.02.003-Up-20.10.2026.7.1 | As-Built DWGs | 135 | 14-Aug-27 | 07-Nov-27 | 04-Dec-27 | 08-May-28 | 0% | 0% | 0.00 |
| JDH1.02.003-Up-20.10.2026.7.2 | Demobilization | 10 | 08-Nov-27 | 18-Nov-27 | 09-May-28 | 20-May-28 | 0% | 0% | 0.00 |

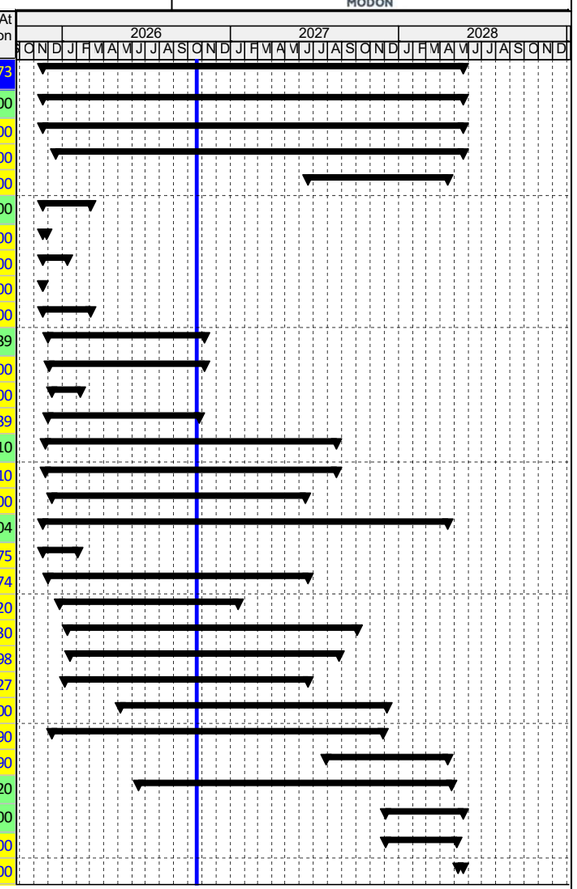


◆ Milestone
summary



TASK filter: All Activities

© Oracle Corporation

19-Oct-26 13:34
