
Activity Name	Schedule % Complete	Physical % Complete
JDH1-02-003 - Infrastructure Development For Industrial City 1 In Jeddah - Update - 20.10.2026		
Milestones		
Contractual Milestone		
Engineering		
Finish Submission and Approval for Shop Drawings, Method of Statement, Prequalification and Materials	100%	0%
Procurement		
Finish PO for Short Lead Item & Long Lead Item	100%	0%
Engineering		
Shop Drawings		
Shop Drawings Submittal		
Shop Drawings Submittal for Electrical Network		
Shop DWG Submittal for Medium Voltage Network	100%	0%
Shop Drawings Approval		
Shop Drawings Approval for Electrical Network		
Shop DWG Approval for Medium Voltage Network	100%	0%
Pre-qualification and Material		
Electrical Network		
Ring Main Unit		
Pre-qualification and Material Approval for Ring Main Unit	100%	30%
Street Lighting Sub-station		
Pre-qualification and Material Approval for Street Lighting Sub-station	100%	30%
Procurement		
Short Lead Item		
Road Works - Civil		
Bituminous Base & Wearing Course		
Material Delivery for Wearing Course	0%	47%
Long Lead Item		
Fence & Gates		
Gates		
Material Fabrication for Gates	100%	20%
Electrical Network		
Cable Termination & Joints		
PO for Cable Termination& Joints	100%	0%
Material Fabrication for Cable Termination & Joints	100%	0%
Medium Voltage Cable		
PO for Medium Voltage Cable	100%	0%
Ring Main Unit		
PO for Ring Main Unit	100%	0%
Bridge Works		
Guard Rail		
Material Delivery for Guard Rail	0%	75%
GRP Panel		
Material Fabrication for GRP Panel	0%	80%
Construction		
Roads & Meduim Voltage		
Local – 01		
LOCAL - 01 Segment-01 (From 0+000 to 1+066)		
Electrical Works		
Approval of Subcontractor / Supplier / Consultant for Medium Voltage from SEC	100%	0%
Approval Materials of Medium Voltage from SEC	100%	0%
Local – 04		
Road Works		
Earthworks and Site Grading		
Excavation for Roadway [Local – 04]	100%	0%
Local – 07		
Road Works		
Earthworks and Site Grading		
Embankments to the parcels for roads [Local – 07]	100%	98%
Deep Infrastructure network		
Local – 01		
LOCAL - 01 Segment-01 (From 0+000 to 1+066)		
Stormwater Utilities		
Manhole		

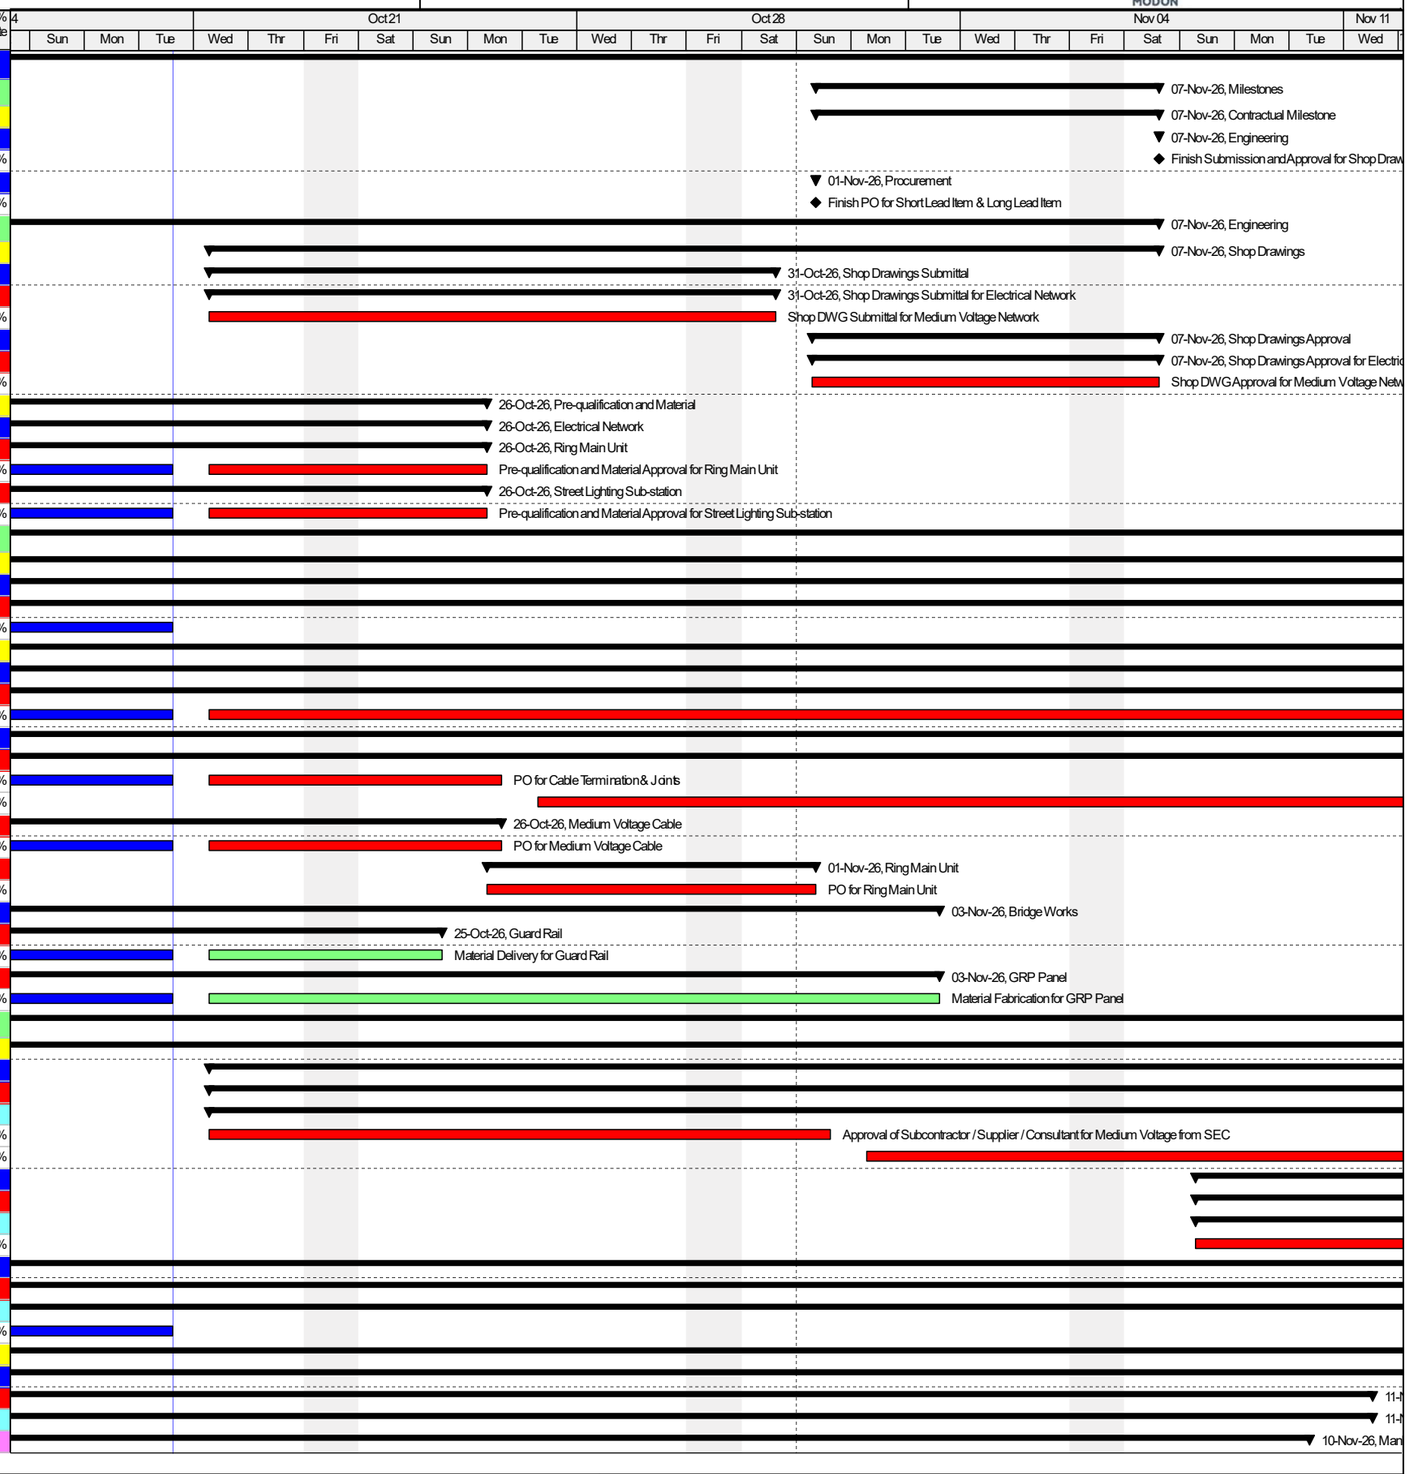


Actual Work | Critical Remaining Work | Summary | Remaining Work | Milestone

TASK filter: Three Week Lookahead -.

© Oracle Corporation

JDH1-02-003 - Infrastructure Development For Industrial City 1 In Jeddah - Update - 20.10.2026

Activity Name	Schedule % Complete	Physical % Complete
Finishing and Testing of Inlet Manholes [Local – 01 Segment-01]	100%	85%
Concrete Chambers/Outfalls		
Finishing and Testing of Concrete chambers [Local – 01 Segment-01]	100%	85%
Sanitary Sewerage		
Manhole		
Installation of Fiberglass Manholes [Local – 01 Segment-01]	100%	95%
LOCAL - 01 Segment-02 (From 1+066 to 2+133)		
Stormwater Utilities		
Concrete Chambers/Outfalls		
Finishing and Testing of Concrete chambers [Local – 01 Segment-02]	100%	95%
Sanitary Sewerage		
Manhole		
Installation of Fiberglass Manholes [Local – 01 Segment-02]	100%	98%
LOCAL - 01 Segment-03 (From 2+133 to 3+200)		
Stormwater Utilities		
Manhole		
Finishing and Testing of Inlet Manholes [Local – 01 Segment-03]	100%	95%
Concrete Chambers/Outfalls		
Finishing and Testing of Concrete chambers [Local – 01 Segment-03]	100%	95%
Sanitary Sewerage		
Manhole		
Installation of Fiberglass Manholes [Local – 01 Segment-03]	100%	95%
Local – 02		
Stormwater Utilities		
Manhole		
Finishing and Testing of Inlet Manholes [Local – 02]	100%	95%
Concrete Chambers/Outfalls		
Finishing and Testing of Concrete chambers [Local – 02]	100%	95%
Sanitary Sewerage		
Manhole		
Installation of Fiberglass Manholes [Local – 02]	100%	95%
Local – 03		
Stormwater Utilities		
Manhole		
Finishing and Testing of Inlet Manholes [Local – 03]	100%	70%
Concrete Chambers/Outfalls		
Finishing and Testing of Concrete chambers [Local – 03]	100%	70%
Local – 04		
Stormwater Utilities		
Manhole		
Installation of Inlet Manholes [Local – 04]	100%	60%
Sanitary Sewerage		
Manhole		
Installation of Fiberglass Manholes [Local – 04]	100%	75%
Local – 05		
Sanitary Sewerage		
Manhole		
Installation of Fiberglass Manholes [Local – 05]	100%	95%
Local – 08		
Stormwater Utilities		
Manhole		
Finishing and Testing of Inlet Manholes [Local – 08]	0%	95%
Concrete Chambers/Outfalls		
Finishing and Testing of Concrete chambers [Local – 08]	0%	95%
Shallow infrastructure network		
Local – 01		
LOCAL - 01 Segment-01 (From 0+000 to 1+066)		
Electrical Works		
Low Voltage		
Excavation works for Low Voltage Cables [Local – 01 Segment-01]	58.82%	80%
Installation of Low Voltage Cables [Local – 01 Segment-01]	0%	80%
Installation of Earthing System [Local – 01 Segment-01]	0%	70%
Telecommunications		
Installation of Reinforced concrete manhole [Local – 01 Segment-01]	0%	90%
Installation of Sand encased duct banks for secondary network [Local – 01 Segment-01]	0%	55%

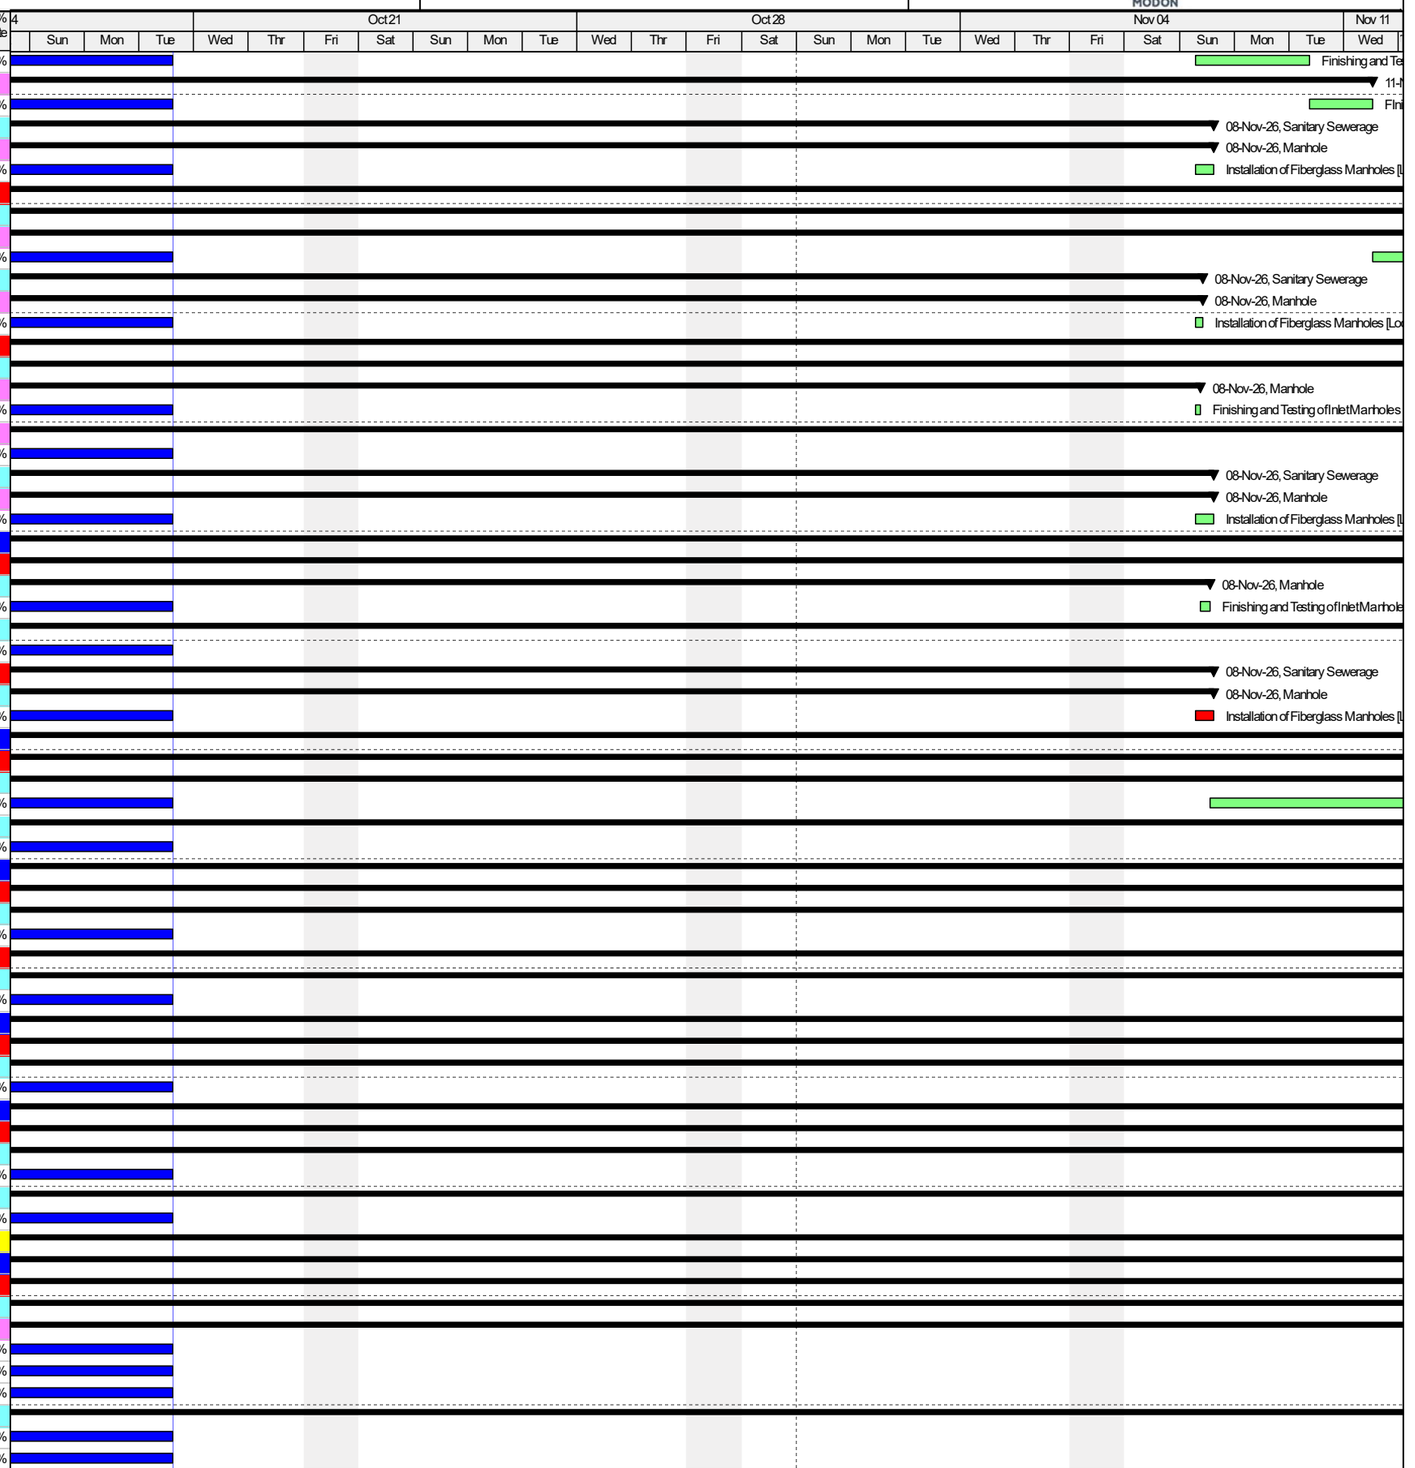


Actual Work · Remaining Work · Critical Remaining Work · Milestone · Summary

TASK filter: Three Week Lookahead -.

© Oracle Corporation

JDH1-02-003 - Infrastructure Development For Industrial City 1 In Jeddah - Update - 20.10.2026

Activity Name	Schedule % Complete	Physical % Complete
Installation of Sand and soil encased duct banks, for combined network of primary and secondary [Local – 01 Segment-01	0%	55%
Installation of Concrete encased duct banks for for combined network of primary and secondary [Local – 01 Segment-01]	0%	55%
CCTV feeding system and GSM		
Excavation works for Low Voltage Cables for CCTV feeding system and GSM [Local – 01 Segment-01]	0%	90%
Installation of Fiber Optic Patch Panel 12 port [Local – 01 Segment-01]	0%	90%
Installation of Modular Industrial Switches for main pole [Local – 01 Segment-01]	0%	90%
Installation of 8POE ports Industrial Switches for remote poles [Local – 01 Segment-01]	0%	90%
Installation of Core Switch [Local – 01 Segment-01]	0%	90%
Installation of Access Switch 48 port [Local – 01 Segment-01]	0%	90%
Installation of Server [Local – 01 Segment-01]	0%	90%
Installation of Stand rack 42U- 19" [Local – 01 Segment-01]	0%	90%
Installation of IP Outdoor CCTV POE Camera,5 MP, Metal Housing [Local – 01 Segment-01]	0%	90%
Installation of Outdoor PTZ IP66 [Local – 01 Segment-01]	0%	90%
Installation of Horizontal Power Distribution Unit (min 8 outlets) [Local – 01 Segment-01]	0%	90%
Installation of Short Range wireless point to point wireless bridge [Local – 01 Segment-01]	0%	90%
Installation of Low Voltage Cables for CCTV feeding system and GSM [Local – 01 Segment-01]	0%	60%
Road Lighting		
Installation of Lighting poles [Local – 01 Segment-01]	0%	90%
Installation of Street Lighting Luminaire [Local – 01 Segment-01]	0%	90%
Installation of Unit Substation Including concrete foundations and fencing [Local – 01 Segment-01]	0%	25%
Installation of Street Lighting feeder pillars / Lighting panels [Local – 01 Segment-01]	0%	90%
Installation of Earthing for Streetlighting feeders for every end pole circuits. [Local – 01 Segment-01]	0%	40%
LOCAL - 01 Segment-02 (From 1+066 to 2+133)		
Electrical Works		
Low Voltage		
Installation of Earthing System [Local – 01 Segment-02]	0%	95%
Earthing System		
Installation of Earthing for Distribution panels,SL feeder pillars ,KWH, Units ubstations and RMU [Local – 01 Segment-02	0%	20%
Road Lighting		
Installation of Earthing for Streetlighting feeders for every end pole circuits. [Local – 01 Segment-02]	0%	70%
LOCAL - 01 Segment-03 (From 2+133 to 3+200)		
TSE Network		
Valves/Chamber		
Installation of Air Valve chambers [Local – 01 Segment-03]	0%	95%
Installation of Wash out chambers [Local – 01 Segment-03]	0%	95%
Public Water Utility Distribution		
Valves/Chamber		
Installation of Air Valve chambers [Local – 01 Segment-03]	0%	95%
Installation of Wash out chambers [Local – 01 Segment-03]	0%	95%
Telecommunications		
Installation of Reinforced concrete manhole [Local – 01 Segment-03]	0%	50%
Installation of Sand and soil encased duct banks for primary network [Local – 01 Segment-03]	0%	60%
Installation of Concrete encased duct banks for primary network [Local – 01 Segment-03]	0%	60%
Installation of Sand encased duct banks for secondary network [Local – 01 Segment-03]	0%	60%
Installation of Sand and soil encased duct banks, for combined network of primary and secondary [Local – 01 Segment-03	0%	60%
Road Lighting		
Installation of Lighting poles [Local – 01 Segment-03]	0%	90%
Installation of Street Lighting Luminaire [Local – 01 Segment-03]	0%	90%
Installation of Street Lighting feeder pillars / Lighting panels [Local – 01 Segment-03]	0%	90%
Installation of Earthing for Streetlighting feeders for every end pole circuits. [Local – 01 Segment-03]	0%	30%
Local – 02		
TSE Network		
Valves/Chamber		
Installation of Wash out Valves [Local – 02]	100%	95%
Installation of Wash out chambers [Local – 02]	100%	95%
Public Water Utility Distribution		
Valves/Chamber		
Installation of Air Valve chambers [Local – 02]	100%	95%
Installation of Gate (Sluice) valves (Direct buried) [Local – 02]	100%	95%
Installation of Wash out chambers [Local – 02]	100%	95%
CCTV feeding system and GSM		
Installation of 8POE ports Industrial Switches for remote poles [Local – 02]	0%	90%
Installation of Server [Local – 02]	0%	90%
Installation of IP Outdoor CCTV POE Camera,5 MP, Metal Housing [Local – 02]	0%	90%
Installation of Outdoor PTZ IP66 [Local – 02]	0%	90%

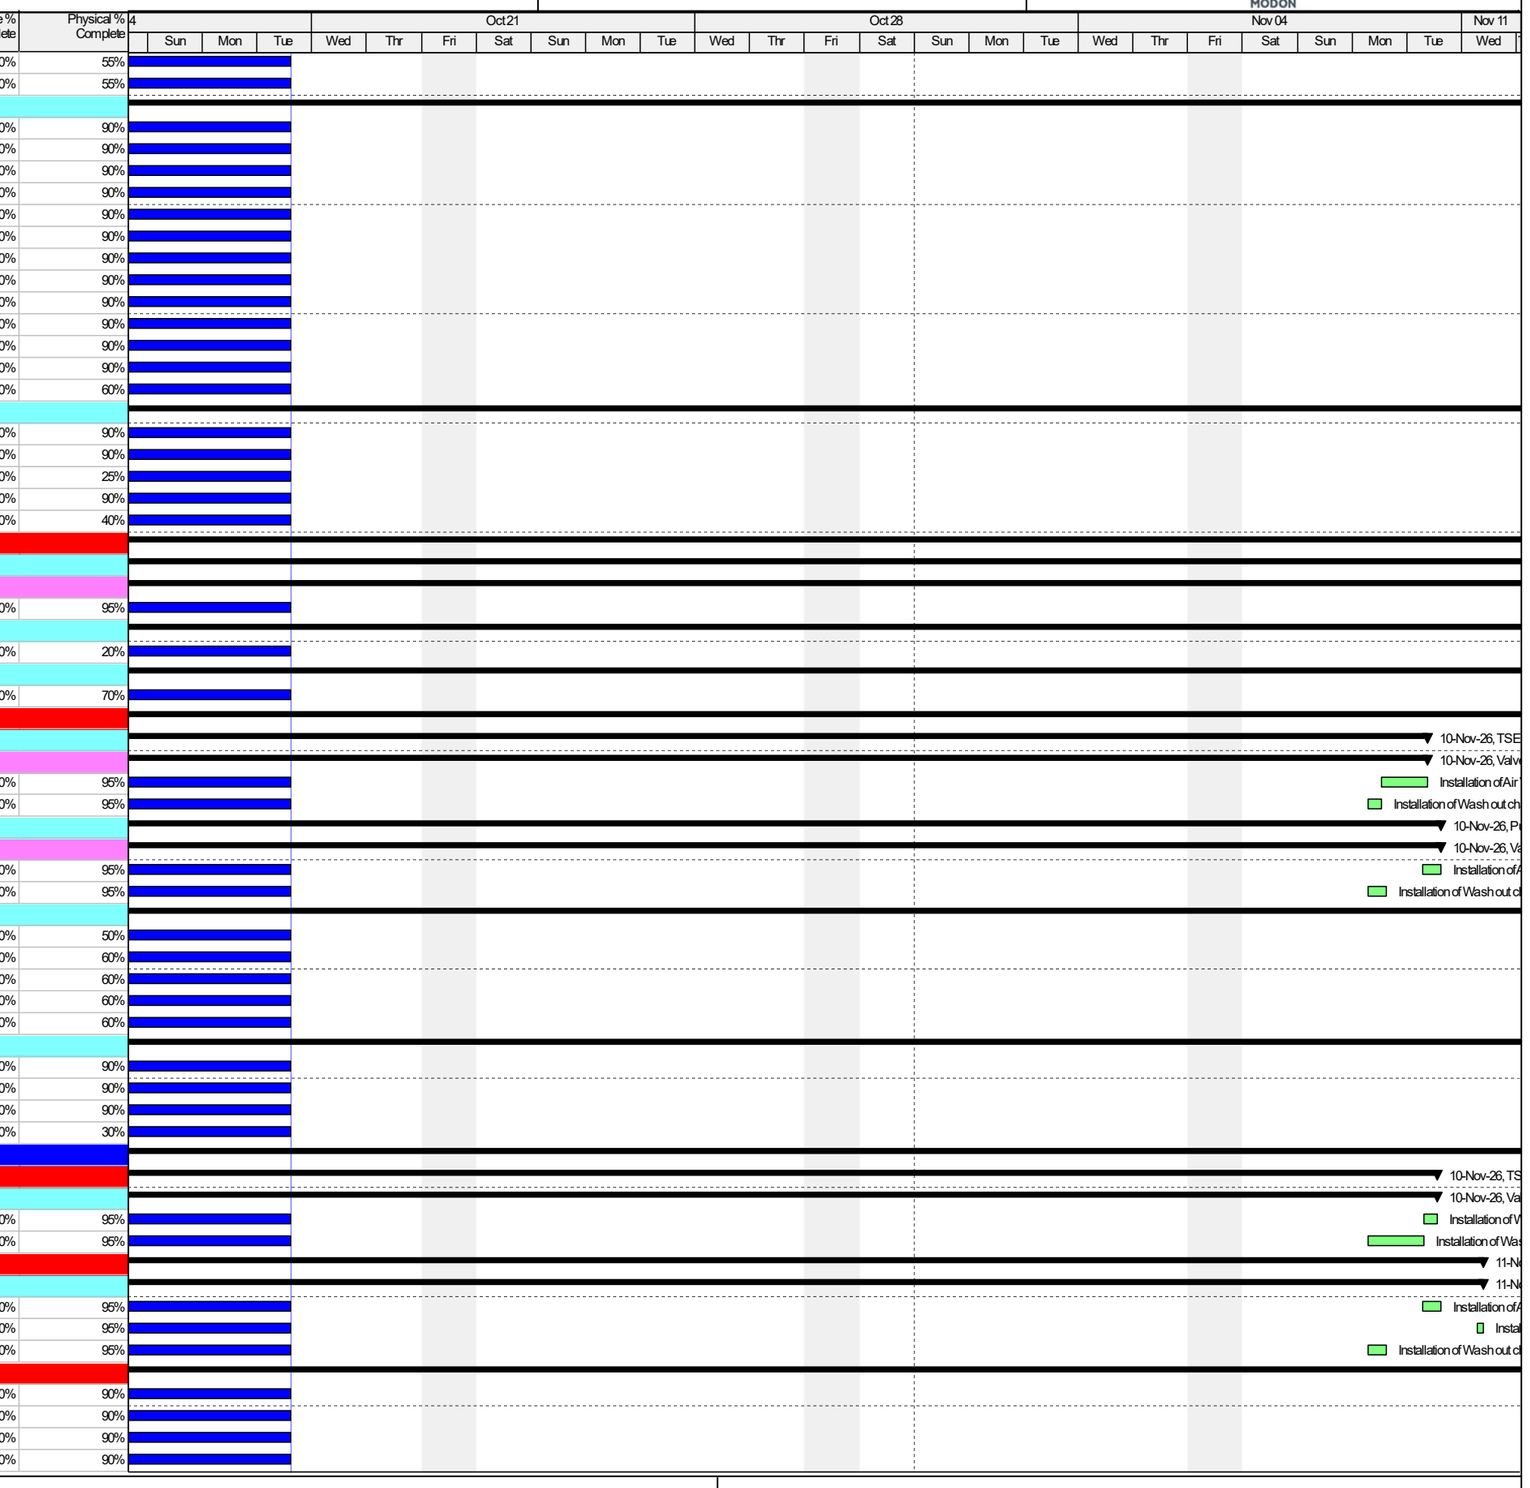


Actual Work | Critical Remaining Work | Summary
Remaining Work | Milestone

TASK filter: Three Week Lookahead -.


© Oracle Corporation

Activity Name	Schedule % Complete	Physical % Complete
Installation of Short Range wireless point to point wireless bridge [Local – 02]	0%	90%
Road Lighting		
Installation of Street Lighting feeder pillars / Lighting panels [Local – 02]	0%	90%
Installation of Earthing for Streetlighting feeders for every end pole circuits. [Local – 02]	0%	50%
Local – 03		
TSE Network		
Valves/Chamber		
Installation of Air Valve chambers [Local – 03]	28.57%	95%
Installation of Wash out chambers [Local – 03]	100%	95%
Public Water Utility Distribution		
Valves/Chamber		
Installation of Air Valve chambers [Local – 03]	0%	95%
Telecommunications		
Installation of Sand and soil encased duct banks for primary network [Local – 03]	0%	30%
Installation of Sand encased duct banks for secondary network [Local – 03]	0%	30%
Installation of Sand and soil encased duct banks, for combined network of primary and secondary [Local – 03]	0%	30%
Installation of Concrete encased duct banks for for combined network of primary and secondary [Local – 03]	0%	30%
CCTV feeding system and GSM		
Installation of Short Range wireless point to point wireless bridge [Local – 03]	0%	90%
Excavation works for Low Voltage Cables for CCTV feeding system and GSM [Local – 03]	0%	90%
Installation of Low Voltage Cables for CCTV feeding system and GSM [Local – 03]	0%	90%
Installation of 8POE ports Industrial Switches for remote poles [Local – 03]	0%	90%
Installation of IP Outdoor CCTV POE Camera,5 MP, Metal Housing [Local – 03]	0%	90%
Installation of Outdoor PTZ IP66 [Local – 03]	0%	90%
Road Lighting		
Installation of Lighting poles [Local – 03]	0%	50%
Installation of Unit Substation Including concrete foundations and fencing [Local – 03]	0%	20%
Installation of Street Lighting Luminaire [Local – 03]	0%	50%
Local – 04		
TSE Network		
Pipe Work		
Excavation for TSE Network [Local – 04]	100%	90%
Granular bedding for TSE Network [Local – 04]	100%	80%
Installation of Pipe for TSE Network [Local – 04]	100%	52%
Granular Surround for TSE Network [Local – 04]	100%	52%
Installation of Micron Marker Magnetic Tape [Local – 04]	100%	52%
Backfilling to Subgrade Elevation [Local – 04]	33.33%	52%
Public Water Utility Distribution		
Pipe Work		
Excavation for Public Water Utility Distribution Piping [Local – 04]	100%	90%
Granular bedding for Public Water Utility Distribution Piping [Local – 04]	100%	80%
Installation of Pipe for Public Water Utility Distribution Piping [Local – 04]	100%	40%
Granular Surround for Public Water Utility Distribution Piping [Local – 04]	100%	40%
Local – 05		
TSE Network		
Valves/Chamber		
Installation of Air Valve chambers [Local – 05]	0%	97%
Installation of Wash out chambers [Local – 05]	38.1%	97%
Public Water Utility Distribution		
Valves/Chamber		
Installation of Wash out chambers [Local – 05]	0%	95%
Telecommunications		
Installation of Reinforced concrete manhole [Local – 05]	0%	90%
Installation of Sand encased duct banks for secondary network [Local – 05]	0%	40%
Installation of Sand and soil encased duct banks, for combined network of primary and secondary [Local – 05]	0%	40%
CCTV feeding system and GSM		
Excavation works for Low Voltage Cables for CCTV feeding system and GSM [Local – 05]	0%	90%
Installation of Low Voltage Cables for CCTV feeding system and GSM [Local – 05]	0%	90%
Installation of Fiber Optic Patch Panel 12 port [Local – 05]	0%	90%
Installation of 8POE ports Industrial Switches for remote poles [Local – 05]	0%	90%
Installation of Core Switch [Local – 05]	0%	90%
Installation of Access Switch 48 port [Local – 05]	0%	90%
Installation of Server [Local – 05]	0%	90%
Installation of IP Outdoor CCTV POE Camera,5 MP, Metal Housing [Local – 05]	0%	90%
Installation of Outdoor PTZ IP66 [Local – 05]	0%	90%

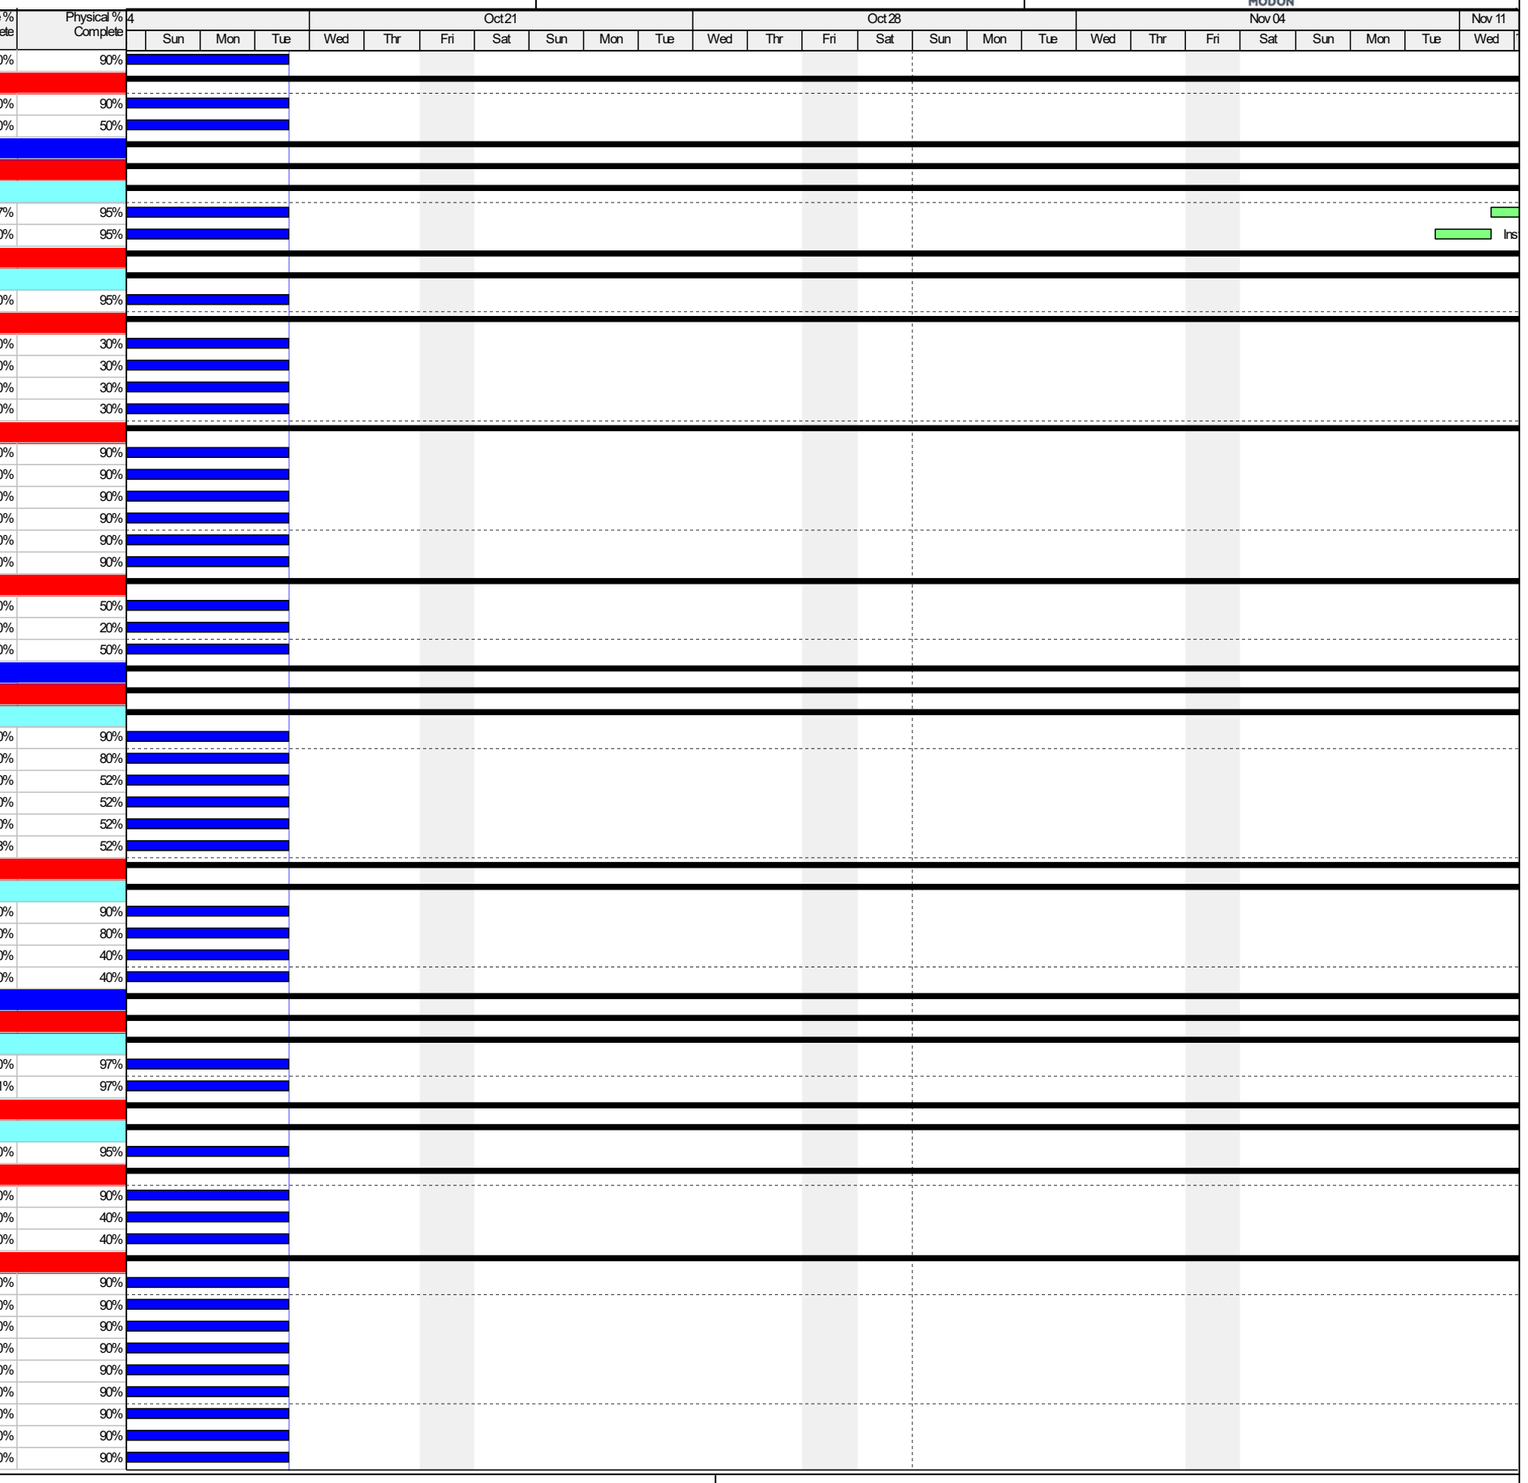


© Oracle Corporation

Activity Name	Schedule % Complete	Physical % Complete
Installation of Horizontal Power Distribution Unit (min 8 outlets) [Local – 05]	0%	90%
Installation of Short Range wireless point to point wireless bridge [Local – 05]	0%	90%
Road Lighting		
Installation of Unit Substation Including concrete foundations and fencing [Local – 05]	0%	30%
Installation of Earthing for Streetlighting feeders for every end pole circuits. [Local – 05]	0%	40%
Local – 06		
Telecommunications		
Installation of Sand encased duct banks for secondary network [Local – 06]	0%	80%
Installation of Sand and soil encased duct banks, for combined network of primary and secondary [Local – 06]	0%	80%
CCTV feeding system and GSM		
Installation of 8POE ports Industrial Switches for remote poles [Local – 06]	0%	90%
Installation of IP Outdoor CCTV POE Camera,5 MP, Metal Housing [Local – 06]	0%	90%
Installation of Outdoor PTZ IP66 [Local – 06]	0%	90%
Installation of Short Range wireless point to point wireless bridge [Local – 06]	0%	90%
Road Lighting		
Installation of Unit Substation Including concrete foundations and fencing [Local – 06]	0%	30%
Installation of Earthing for Streetlighting feeders for every end pole circuits. [Local – 06]	0%	30%
Local – 07		
CCTV feeding system and GSM		
Installation of Short Range wireless point to point wireless bridge [Local – 07]	0%	90%
Road Lighting		
Installation of Unit Substation Including concrete foundations and fencing [Local – 07]	0%	40%
Installation of Earthing for Streetlighting feeders for every end pole circuits. [Local – 07]	0%	50%
Local – 08		
TSE Network		
Valves/Chamber		
Installation of Air Valve chambers [Local – 08]	0%	95%
Installation of Wash out chambers [Local – 08]	0%	95%
CCTV feeding system and GSM		
Installation of Outdoor PTZ IP66 [Local – 08]	0%	90%
Installation of Short Range wireless point to point wireless bridge [Local – 08]	0%	90%
Road Lighting		
Installation of Lighting poles [Local – 08]	0%	90%
Installation of Unit Substation Including concrete foundations and fencing [Local – 08]	0%	30%
Installation of Street Lighting Luminaire [Local – 08]	0%	90%
Installation of Street Lighting feeder pillars / Lighting panels [Local – 08]	0%	90%
Bridge		
Bridge Finishing		
Membrane waterproofing for concert in touch with soil and membrane waterproofing for bridge slab [Bridge]	0%	0%
Placing of Protective Coating for Concrete Surfaces [Bridge]	0%	0%
Outside Boundary Area (Tie-in Lines)		
Sanitary Sewerage		
Manhole		
Installation of Fiberglass Manholes [Outside Boundary Area]	100%	95%
TSE Network		
Valves/Chamber		
Installation of Valve Chamber [Outside Boundary Area]	0%	98%
Installation of Butterfly valves (In Chamber) [Outside Boundary Area]	0%	98%
Public Water Utility Distribution		
Public Water Utility Distribution (0 - 900) m		
Valves/Chamber		
Installation of Air Valves [Outside Boundary Area] 0 - 900 m	100%	95%
Installation of Air Valve chambers [Outside Boundary Area] 0 - 900 m	100%	95%
Public Water Utility Distribution (901 - 1800) m		
Valves/Chamber		
Installation of Air Valve chambers [Outside Boundary Area] 901 - 1800 m	0%	98%
Installation of Air Valves [Outside Boundary Area] 901 - 1800 m	0%	98%
Installation of Butterfly valves, on pipe with diameter 400 mm	0%	98%
Roads Finishing		
Local – 01		
LOCAL - 01 Segment-01 (From 0+000 to 1+066)		
Concrete Curb		
Installation of Precast Concrete Curb [Local – 01 Segment-01]	0%	90%
Asphalt Wearing Course		
Tack coat (RC2) [Local – 01 Segment-01]	0%	45%

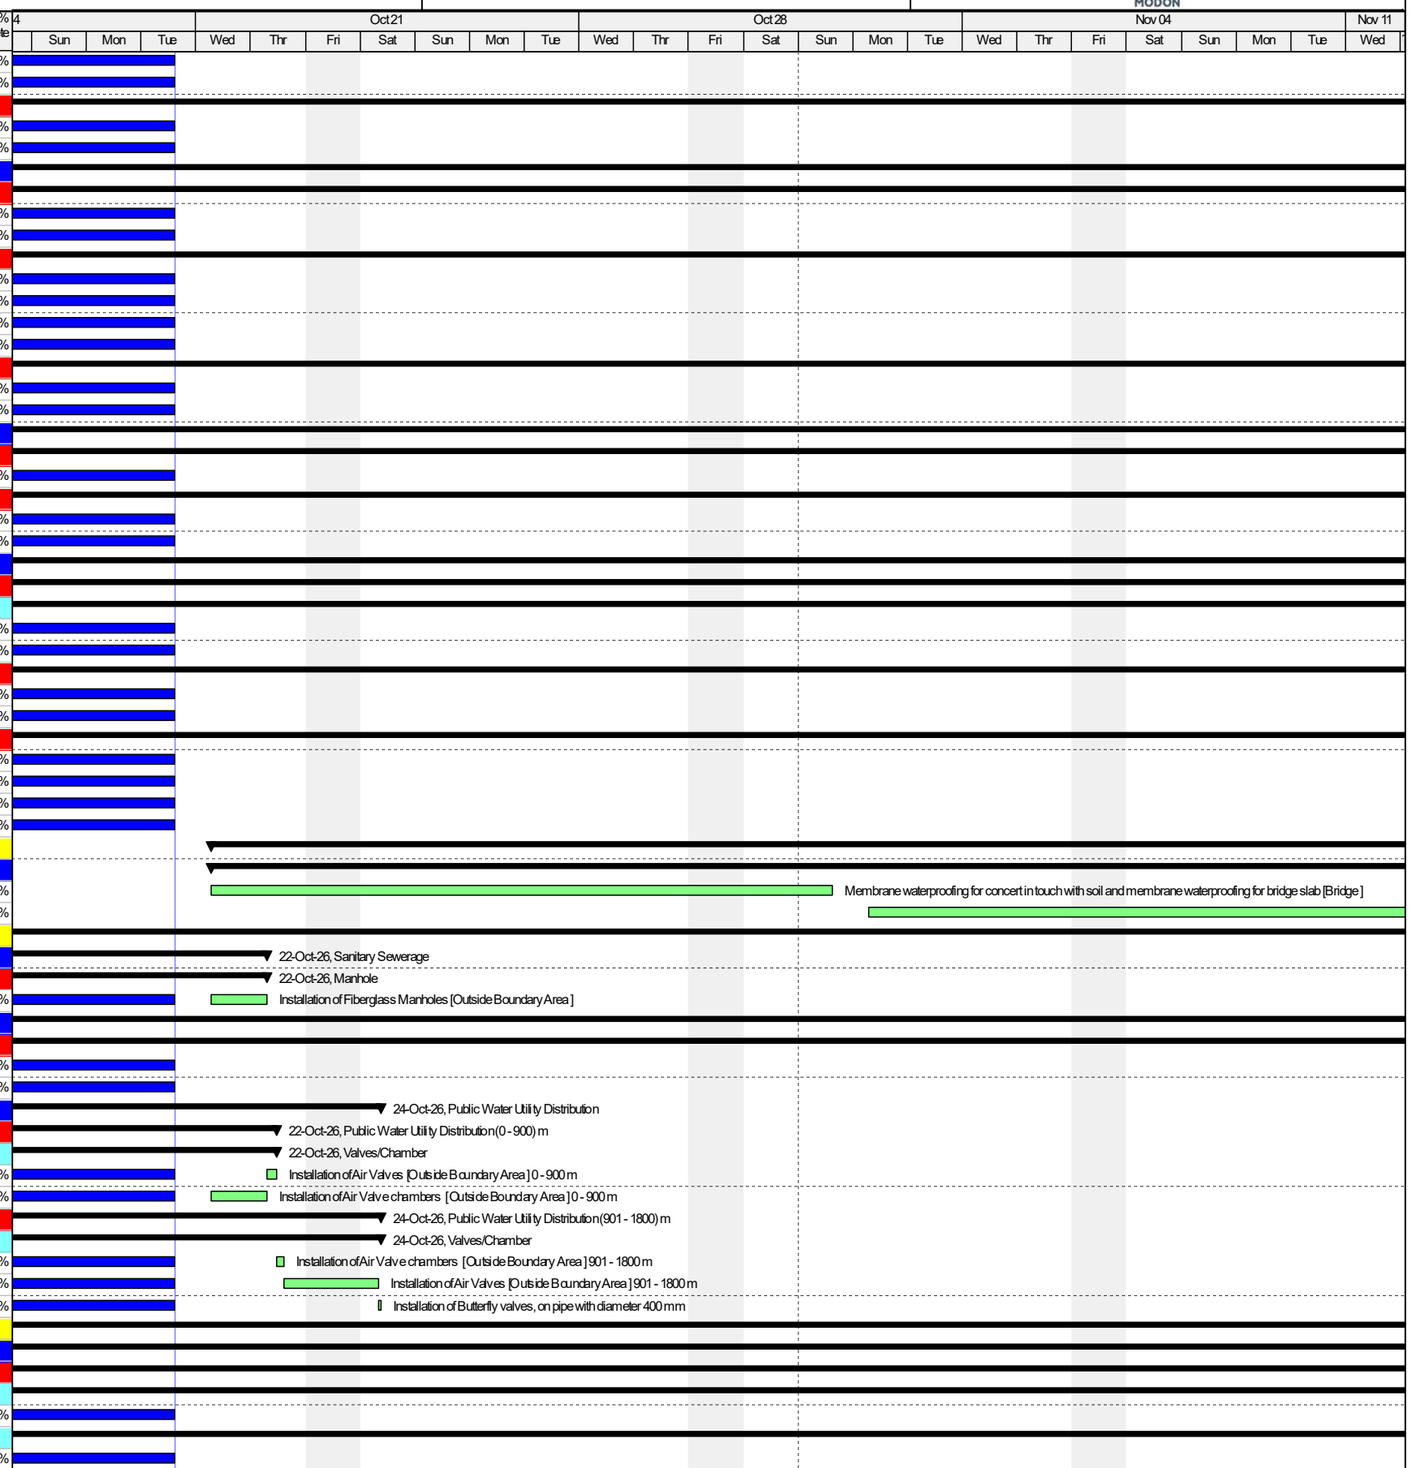

© Oracle Corporation

Activity Name	Schedule % Complete	Physical % Complete
Bituminous wearing course [Local – 01 Segment-01]	0%	45%
Interlocking block sidewalk/footpath		
Interlocking block pavers for sidewalk/footpath [Local – 01 Segment-01]	0%	60%
Traffic Signs		
Installation of Traffic Signs [Local – 01 Segment-01]	0%	60%
LOCAL - 01 Segment-02 (From 1+066 to 2+133)		
Asphalt Wearing Course		
Tack coat (RC2) [Local – 01 Segment-02]	0%	70%
Bituminous wearing course [Local – 01 Segment-02]	0%	70%
Traffic Signs		
Installation of Traffic Signs [Local – 01 Segment-02]	0%	75%
LOCAL - 01 Segment-03 (From 2+133 to 3+200)		
Traffic Signs		
Installation of Traffic Signs [Local – 01 Segment-03]	0%	75%
Local – 02		
Asphalt Wearing Course		
Tack coat (RC2) [Local – 02]	0%	90%
Bituminous wearing course [Local – 02]	0%	90%
Traffic Signs		
Installation of Traffic Signs [Local – 02]	0%	75%
Local – 03		
Concrete Curb		
Installation of Precast Concrete Curb [Local – 03]	0%	75%
Interlocking block sidewalk/footpath		
Interlocking block pavers for sidewalk/footpath [Local – 03]	0%	10%
Traffic Signs		
Installation of Traffic Signs [Local – 03]	0%	30%
Local – 05		
Asphalt Wearing Course		
Tack coat (RC2) [Local – 05]	0%	85%
Bituminous wearing course [Local – 05]	0%	85%
Traffic Signs		
Installation of Traffic Signs [Local – 05]	0%	75%
Local – 06		
Asphalt Wearing Course		
Tack coat (RC2) [Local – 06]	0%	60%
Bituminous wearing course [Local – 06]	0%	60%
Traffic Signs		
Installation of Traffic Signs [Local – 06]	0%	75%
Local – 07		
Asphalt Wearing Course		
Tack coat (RC2) [Local – 07]	0%	90%
Bituminous wearing course [Local – 07]	0%	90%
Traffic Signs		
Installation of Traffic Signs [Local – 07]	0%	75%
Local – 08		
Traffic Signs		
Installation of Traffic Signs [Local – 08]	0%	75%
Fence and Gate		
Fence and Gate Segment -01 (From 0+000 to 0+671)		
Fence		
Excavation for Fences [Fence and Gate Segment -01]	100%	85%
Lean concrete for Foundation [Fence and Gate Segment -01]	100%	20%
Reinforced concrete Structure [Fence and Gate Segment -01]	100%	20%
Fence and Gate Segment -02 (From 0+671 to 1+342)		
Fence		
Excavation for Fences [Fence and Gate Segment -02]	100%	85%
Lean concrete for Foundation [Fence and Gate Segment -02]	100%	85%
Reinforced concrete Structure [Fence and Gate Segment -02]	100%	85%
Spraying of bituminous paint waterproofing for R.C foundation [Fence and Gate Segment -02]	100%	85%
Embankments to the Fences [Fence and Gate Segment -02]	100%	85%
Concrete Works for Ground Beam for Fences [Fence and Gate Segment -02]	100%	85%
Installation of Metal Fence [Fence and Gate Segment -02]	100%	40%
Fence and Gate Segment -03 (From 1+342 to 2+014)		
Fence		

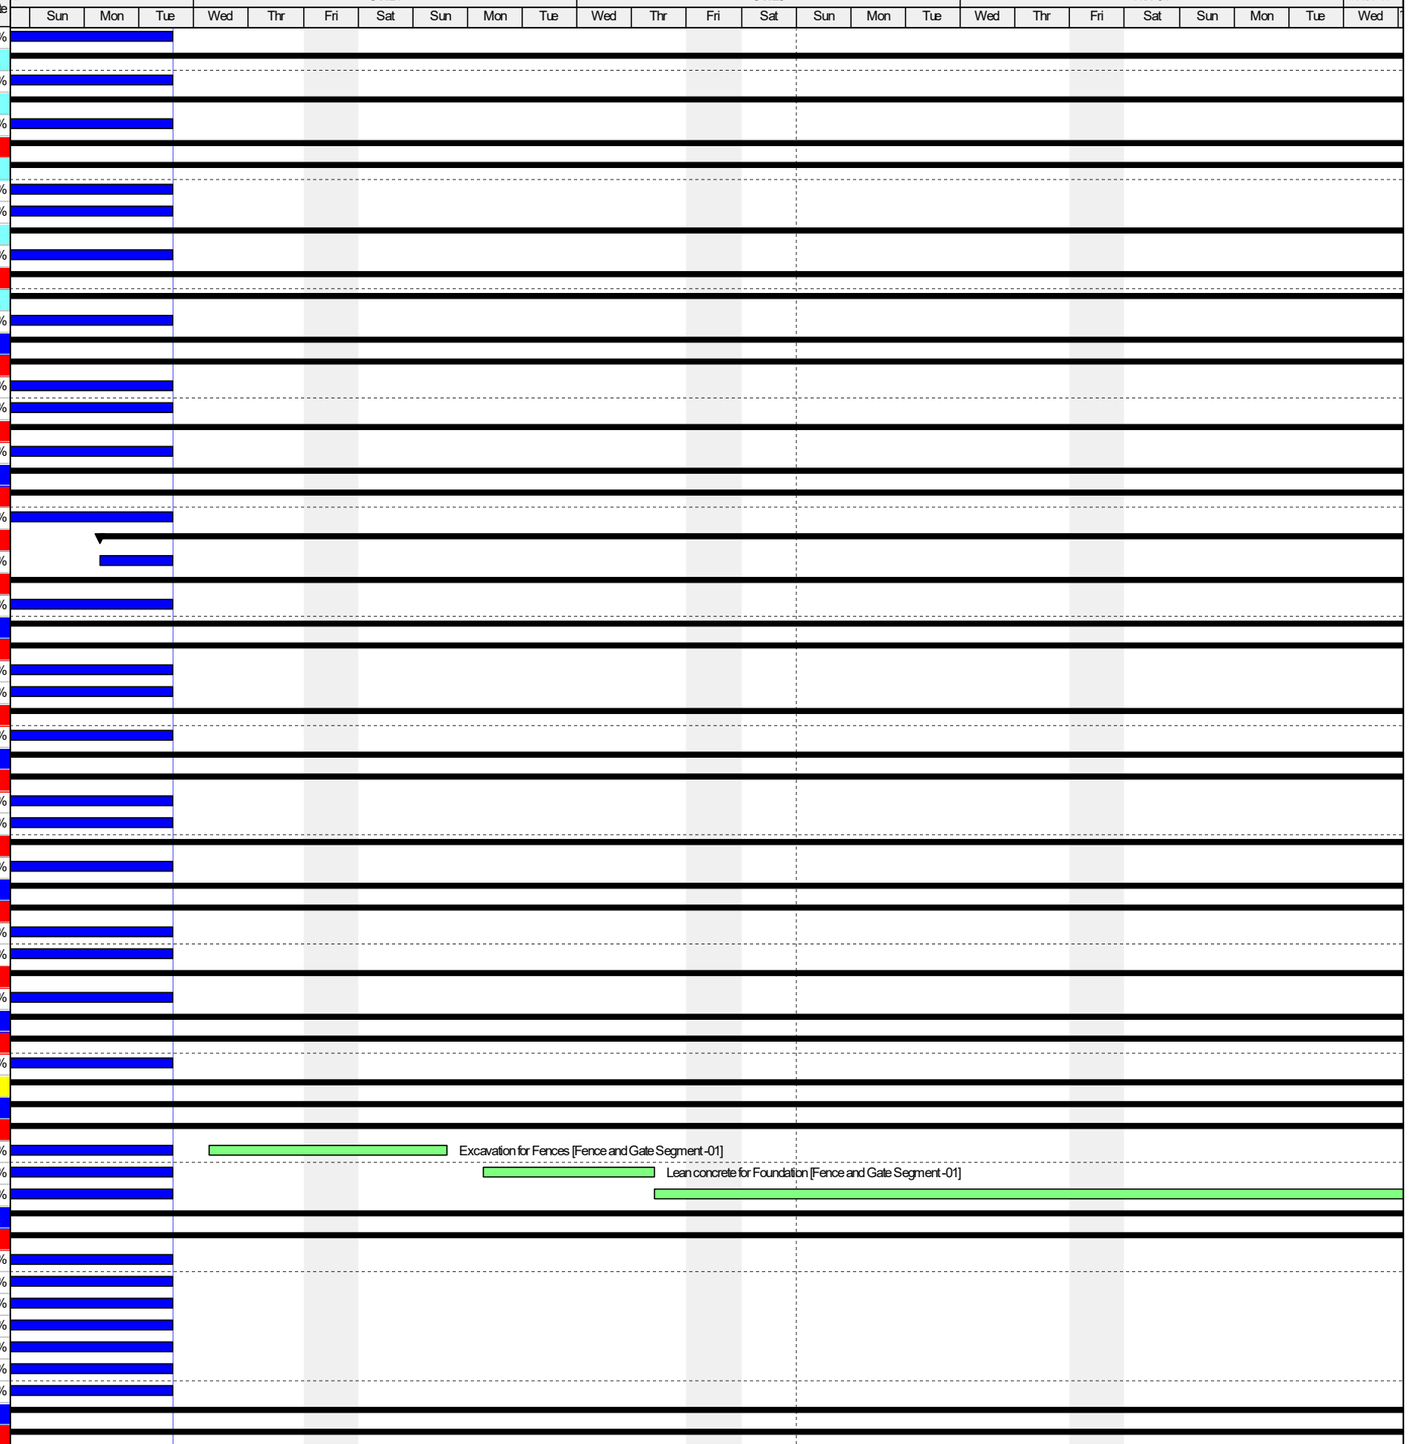

Actual Work
Remaining Work
Critical Remaining Work
Milestone
Summary

TASK filter: Three Week Lookahead -.

© Oracle Corporation

ENJAZCO


Tel.:4108184 - 4108180
Email: info@enjaz-co.com

JDH1-02-003 - Infrastructure Development For Industrial City 1 In Jeddah - Update - 20.10.2026

egis

MODON

Activity Name	Schedule % Complete	Physical % Complete
Installation of Metal Fence [Fence and Gate Segment -03]	0%	97%
Plster Works for Fences [Fence and Gate Segment -03]	0%	40%
Paint On Cement Plaster [Fence and Gate Segment -03]	0%	40%
Fence and Gate Segment -04 (From 2+014 to 2+685)		
Fence		
Paint On Cement Plaster [Fence and Gate Segment -04]	0%	95%
Plster Works for Fences [Fence and Gate Segment -04]	0%	95%
Testing & Commissioning		
Test for Public Water Utility Distribution	0%	80%
Test for TSE Network	0%	80%
Test for Sanitary Sewerage	0%	75%
Test for Stormwater Utilities	0%	75%
Test for Bridge Work	0%	65%
Test for Fence & Gate	0%	60%
Test for Telecommunications Work	0%	30%
Test for Electrical Network	0%	40%
Test for CCTV feeding system and GSM	0%	40%
Test for Road Lighting	0%	40%
Test for Road Works	0%	70%
Test for Earthing System	0%	30%

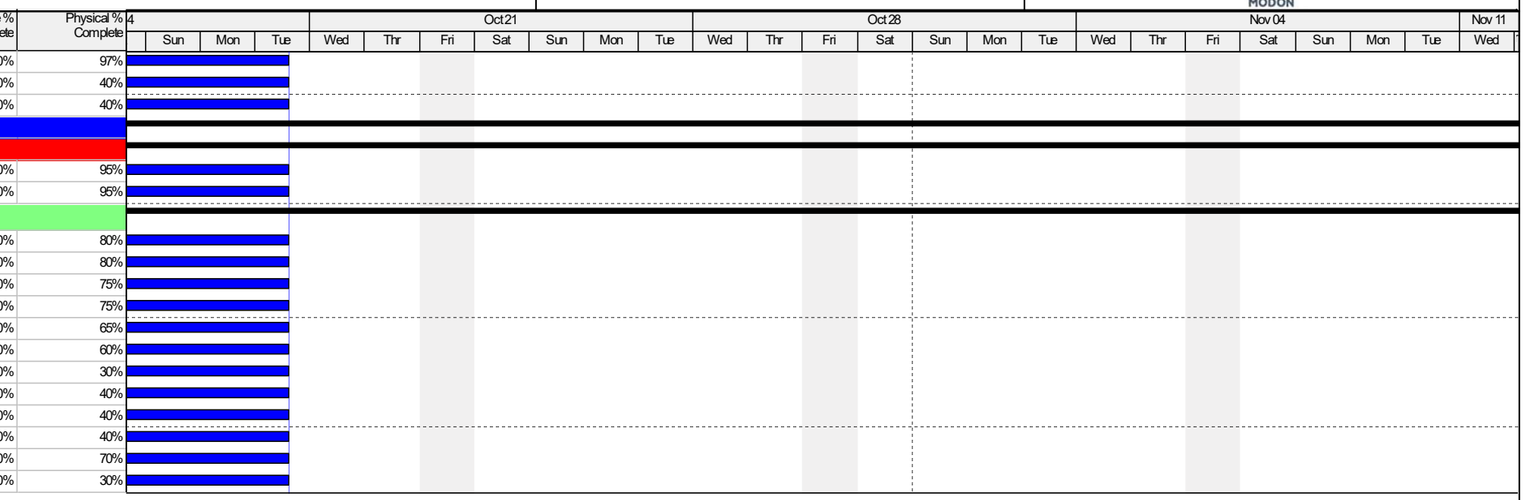

Actual Work
Remaining Work
Critical Remaining Work
Milestone
Summary

TASK filter: Three Week Lookahead -.

© Oracle Corporation
