
	ADDITIONAL DEVELOPMENT IN TABOUK INDUSTRIAL CITY	Progress Certificate # 01		

Activity ID	Activity Name	Original Duration	BL Project Start	BL Project Finish	Start	Finish	Performance % Complete	Performance % Complete - Labor Units	Budget At Completion
3066	ADDITIONAL DEVELOPMENT IN TABOUK INDUSTRIAL CITY	651	04-Sep-25	03-Sep-27	04-Sep-25 A	02-Oct-27	46.89%	46%	$140,467,862.00
3066.GENERAL	MILESTONS	651	04-Sep-25	03-Sep-27	04-Sep-25 A	02-Oct-27	0%	0%	$0.00
3066.GENERAL.2	CONTRACTUAL MILESTONES	651	04-Sep-25	03-Sep-27	04-Sep-25 A	02-Oct-27	0%	0%	$0.00
3066.GENERAL.1	NET WORK MILESTONES	620	11-Oct-25	03-Sep-27	11-Oct-25 A	02-Oct-27	0%	0%	$0.00
3066.GENERAL.4	ZONES MILESTONES	585	04-Sep-25	15-Aug-27	04-Sep-25 A	18-Jul-27	0%	0%	$0.00
3066.GENERAL.3	PRELIMINARY SUBMITTALS	229	09-Sep-25	02-Jun-26	09-Sep-25 A	03-Nov-26	0%	0%	$0.00
3066.5	MOBILIZATION	632	04-Sep-25	23-Aug-27	04-Sep-25 A	30-Aug-27	0%	100%	$0.00
3066.5.2	Site Facilites and Offices	632	04-Sep-25	23-Aug-27	04-Sep-25 A	30-Aug-27	0%	100%	$0.00
3066.5.1	Preliminaries	36	25-Nov-25	05-Jan-26	25-Nov-25 A	05-Jan-26 A	0%	0%	$0.00
3066.6	ENGINEERING	208	04-Oct-25	02-Jun-26	04-Oct-25 A	02-Jun-26 A	100%	0%	$4,214,035.86
3066.6.2	Shop Drawings Submittls	193	21-Oct-25	02-Jun-26	21-Oct-25 A	02-Jun-26 A	100%	0%	$4,214,035.86
3066.6.3	Prequalification for Suppliers	174	04-Oct-25	23-Apr-26	04-Oct-25 A	23-Apr-26 A	0%	0%	$0.00
3066.6.4	Method Statement	124	25-Nov-25	18-Apr-26	25-Nov-25 A	18-Apr-26 A	0%	0%	$0.00
3066.17	PROCUREMENT	604	27-Oct-25	02-Sep-27	27-Oct-25 A	29-Sep-27	60.62%	0%	$28,093,572.39
3066.17.8	Material Purchase Order	283	01-Nov-25	08-Sep-26	01-Nov-25 A	25-Jul-26 A	0%	0%	$0.00
3066.17.17	Material Fabrication and Delivery	604	27-Oct-25	02-Sep-27	27-Oct-25 A	29-Sep-27	60.62%	0%	$28,093,572.39
3066.1	CONSTRUCTION WORKS	651	04-Sep-25	03-Sep-27	04-Sep-25 A	02-Oct-27	47.42%	46.41%	$94,113,467.75
3066.1.9	ZONE 1	611	21-Oct-25	03-Sep-27	21-Oct-25 A	02-Oct-27	60.04%	53.4%	$19,581,738.06
3066.1.10	ZONE 2	579	11-Oct-25	11-Aug-27	11-Oct-25 A	16-Aug-27	55.89%	57.64%	$25,906,629.88
3066.1.11	ZONE 3	647	04-Sep-25	30-Aug-27	04-Sep-25 A	27-Sep-27	37.82%	36.88%	$48,625,099.81
3066.22	CLOSE OUT	198	17-Apr-27	03-Sep-27	14-Feb-27	02-Oct-27	0%	0%	$14,046,786.00
3066.22.3	Final Testing and Commmisionning	176	17-Apr-27	03-Sep-27	14-Feb-27	06-Sep-27	0%	0%	$13,562,866.00
3066.22.2	AS BUILT DRAWINGS	168	19-Jul-27	16-Aug-27	02-Mar-27	13-Sep-27	0%	0%	$483,920.00
3066.22.1	DEMOBILIZATION	16	17-Aug-27	03-Sep-27	13-Sep-27	02-Oct-27	0%	0%	$0.00

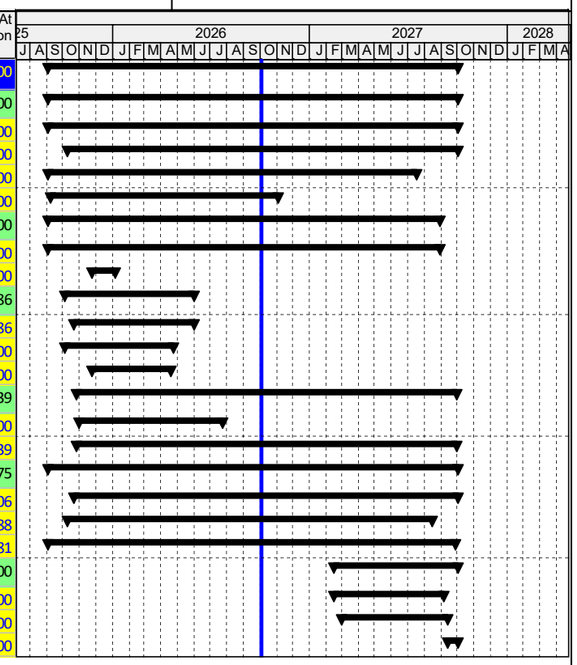

© Oracle Corporation
