
egis | ENJAZCO شركة الانجاز للتجارة والمقاولات AlEnjaz Company For Trading And Contracting

JDH4-02-007-R-UP-Land Development of Jeddah Oasis- 06 Oct 2026
2 Week Look Ahead

MODON

Activity ID	Activity Name	Original Duration	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Schedule % Complete	Performance % Complete	Variance - BL Project Finish Date
JDH4-02-007-R-UP-Land Developmen		178	23-Mar-26	06-May-27	16-May-26 A	03-Jan-27	15,196.90	4,258,451.33	8,633,457.25	0.18%	49.32%	102
Key Milestones		0	23-Mar-26	22-Sep-26	06-Oct-26	06-Oct-26	0.00	0.00	0.00	0%	0%	-11
Contractual Milestone		0	23-Mar-26	22-Sep-26	06-Oct-26	06-Oct-26	0.00	0.00	0.00	0%	0%	-11
Construction		0	23-Mar-26	22-Sep-26	06-Oct-26	06-Oct-26	0.00	0.00	0.00	0%	0%	-11
JDH4-02-007-M	Completion of Road Works	0		22-Sep-26		06-Oct-26	0.00	0.00	0.00	100%	0%	-11
JDH4-02-007-M	Completion of Earthworks & Site Gra	0		23-Mar-26		06-Oct-26	0.00	0.00	0.00	100%	0%	-165
Construction		178	24-Sep-26	06-May-27	16-May-26 A	30-Dec-26	15,196.90	3,644,476.18	6,177,556.63	0.25%	59%	105
Roads		25	24-Sep-26	23-Nov-26	07-Oct-26	04-Nov-26	15,196.90	0.00	174,616.91	8.7%	0%	16
Road 01		25	24-Sep-26	23-Nov-26	07-Oct-26	04-Nov-26	15,196.90	0.00	137,983.13	11.01%	0%	16
Road Works (Roundabout)		25	24-Sep-26	23-Nov-26	07-Oct-26	04-Nov-26	15,196.90	0.00	137,983.13	11.01%	0%	16
Finishing Works		25	24-Sep-26	23-Nov-26	07-Oct-26	04-Nov-26	15,196.90	0.00	137,983.13	11.01%	0%	16
Asphalt Wearing Course		25	24-Sep-26	22-Oct-26	07-Oct-26	04-Nov-26	15,196.90	0.00	95,937.28	15.84%	0%	-11
JDH4-02-00	Bituminous concrete wearing course	15	06-Oct-26	22-Oct-26	19-Oct-26	04-Nov-26	5,767.17	0.00	86,507.55	6.67%	0%	-11
JDH4-02-00	Tack Coat (RC2) [Road 01]	10	24-Sep-26	05-Oct-26	07-Oct-26	18-Oct-26	9,429.73	0.00	9,429.73	100%	0%	-11
Pavement Markings		4	05-Nov-26	09-Nov-26	07-Oct-26	11-Oct-26	0.00	0.00	16,149.78	0%	0%	25
JDH4-02-00	Pavement markings [Road 01]	4	05-Nov-26	09-Nov-26	07-Oct-26	11-Oct-26	0.00	0.00	16,149.78	0%	0%	25
Traffic Signage		12	10-Nov-26	23-Nov-26	12-Oct-26	25-Oct-26	0.00	0.00	25,896.07	0%	0%	25
JDH4-02-00	Installation of Traffic Signs [Road 01]	12	10-Nov-26	23-Nov-26	12-Oct-26	25-Oct-26	0.00	0.00	25,896.07	0%	0%	25
Road 10		22	17-Oct-26	22-Nov-26	07-Oct-26	01-Nov-26	0.00	0.00	36,633.78	0%	0%	18
Electrical Works		22	17-Oct-26	22-Nov-26	07-Oct-26	01-Nov-26	0.00	0.00	36,633.78	0%	0%	18
MV & LV Cables		22	17-Oct-26	22-Nov-26	07-Oct-26	01-Nov-26	0.00	0.00	36,633.78	0%	0%	18
Low Voltage Cable		22	17-Oct-26	22-Nov-26	07-Oct-26	01-Nov-26	0.00	0.00	36,633.78	0%	0%	18
JDH4-02-00	Excavation for Low Voltage Cable [R	11	17-Oct-26	28-Oct-26	07-Oct-26	19-Oct-26	0.00	0.00	9,839.72	0%	0%	8
JDH4-02-00	Installation of Low Voltage Cables [R	11	10-Nov-26	22-Nov-26	20-Oct-26	01-Nov-26	0.00	0.00	26,794.06	0%	0%	18
Sewage Lift Station		150	08-Dec-26	02-May-27	17-Sep-26 A	30-Dec-26	0.00	262,851.09	1,491,787.73	0%	17.62%	101
Mechanical Works		69	08-Dec-26	10-Jan-27	23-Sep-26 A	21-Oct-26	0.00	211,617.10	1,179,505.13	0%	17.94%	69
Interface Works		3	08-Dec-26	10-Dec-26	07-Oct-26	10-Oct-26	0.00	0.00	63,075.14	0%	0%	53
JDH4-02-007-	Interfacing Works [Sewage Lift Statio	3	08-Dec-26	10-Dec-26	07-Oct-26	10-Oct-26	0.00	0.00	63,075.14	0%	0%	53
Anti Water Hammer Equipment		4	12-Dec-26	15-Dec-26	01-Oct-26 A	14-Oct-26	0.00	176,610.39	883,051.97	0%	20%	53
JDH4-02-007-	Installation of Anti-Water Hammer Ec	4	12-Dec-26	15-Dec-26	01-Oct-26 A	14-Oct-26	0.00	176,610.39	883,051.97	0%	20%	53
Pumps		6	04-Jan-27	10-Jan-27	23-Sep-26 A	21-Oct-26	0.00	35,006.70	233,378.02	0%	15%	69
JDH4-02-007-	Installation of Submersible pump [Se	6	04-Jan-27	10-Jan-27	23-Sep-26 A	21-Oct-26	0.00	35,006.70	233,378.02	0%	15%	69
Electrical Works		147	12-Dec-26	02-May-27	17-Sep-26 A	30-Dec-26	0.00	51,234.00	312,282.60	0%	16.41%	101
Main Distribution Board		14	12-Dec-26	27-Dec-26	11-Oct-26	26-Oct-26	0.00	0.00	104,073.98	0%	0%	53
JDH4-02-007-	Installation of Panel Board [Sewage I	7	20-Dec-26	27-Dec-26	19-Oct-26	26-Oct-26	0.00	0.00	28,383.81	0%	0%	53
JDH4-02-007-	Installation of Main Distribution Board	7	12-Dec-26	19-Dec-26	11-Oct-26	18-Oct-26	0.00	0.00	75,690.17	0%	0%	53
Local Control Panel		10	20-Dec-26	30-Dec-26	19-Oct-26	29-Oct-26	0.00	0.00	25,230.06	0%	0%	53
JDH4-02-007-	Installation of MCP-LP-01 [Sewage L	10	20-Dec-26	30-Dec-26	19-Oct-26	29-Oct-26	0.00	0.00	25,230.06	0%	0%	53
Instrumentation for Process Systems		8	21-Apr-27	02-May-27	17-Sep-26 A	30-Dec-26	0.00	51,234.00	182,978.56	0%	28%	101
JDH4-02-007-	Installation of Process System [Sewa	8	21-Apr-27	02-May-27	17-Sep-26 A	30-Dec-26	0.00	51,234.00	182,978.56	0%	28%	101
MV Cable Works		29	07-Mar-27	06-May-27	20-Jun-26 A	16-Dec-26	0.00	176,668.34	196,298.15	0%	90%	117
Medium Voltage Cable Out of Zone		29	07-Mar-27	06-May-27	20-Jun-26 A	16-Dec-26	0.00	176,668.34	196,298.15	0%	90%	117
JDH4-02-007-C	Excavation for Trench [Out of Zone]	21	07-Mar-27	03-Apr-27	20-Jun-26 A	10-Dec-26	0.00	8,312.51	9,236.12	0%	90%	94
JDH4-02-007-C	Installation of Duct banks [Out of Zone	16	04-Apr-27	21-Apr-27	25-Jul-26 A	14-Dec-26	0.00	29,973.31	33,303.68	0%	90%	107
JDH4-02-007-C	Installation of Medium Voltage Cable	13	22-Apr-27	06-May-27	03-Aug-26 A	16-Dec-26	0.00	138,382.52	153,758.35	0%	90%	117
Plot Backfilling 2		20	14-Jan-27	06-Feb-27	25-Jul-26 A	19-Oct-26	0.00	1,317,819.91	2,027,415.24	0%	65%	94
JDH4-02-007-CI	Plots backfilling Stage 7 [Plots]	10	26-Jan-27	06-Feb-27	30-Jul-26 A	19-Oct-26	0.00	608,224.57	1,013,707.62	0%	60%	94
JDH4-02-007-CI	Plots backfilling Stage 6 [Plots]	10	14-Jan-27	25-Jan-27	25-Jul-26 A	13-Oct-26	0.00	709,595.33	1,013,707.62	0%	70%	90
Additional Works		30	25-Mar-27	24-Apr-27	16-May-26 A	25-Oct-26	0.00	1,887,136.84	2,287,438.60	0%	82.5%	152
JDH4-02-007-CI	Road Work	25	27-Mar-27	24-Apr-27	16-May-26 A	19-Oct-26	0.00	972,161.40	1,143,719.30	0%	85%	157
JDH4-02-007-CI	Electrical Works	25	25-Mar-27	22-Apr-27	28-Jun-26 A	25-Oct-26	0.00	914,975.44	1,143,719.30	0%	80%	151

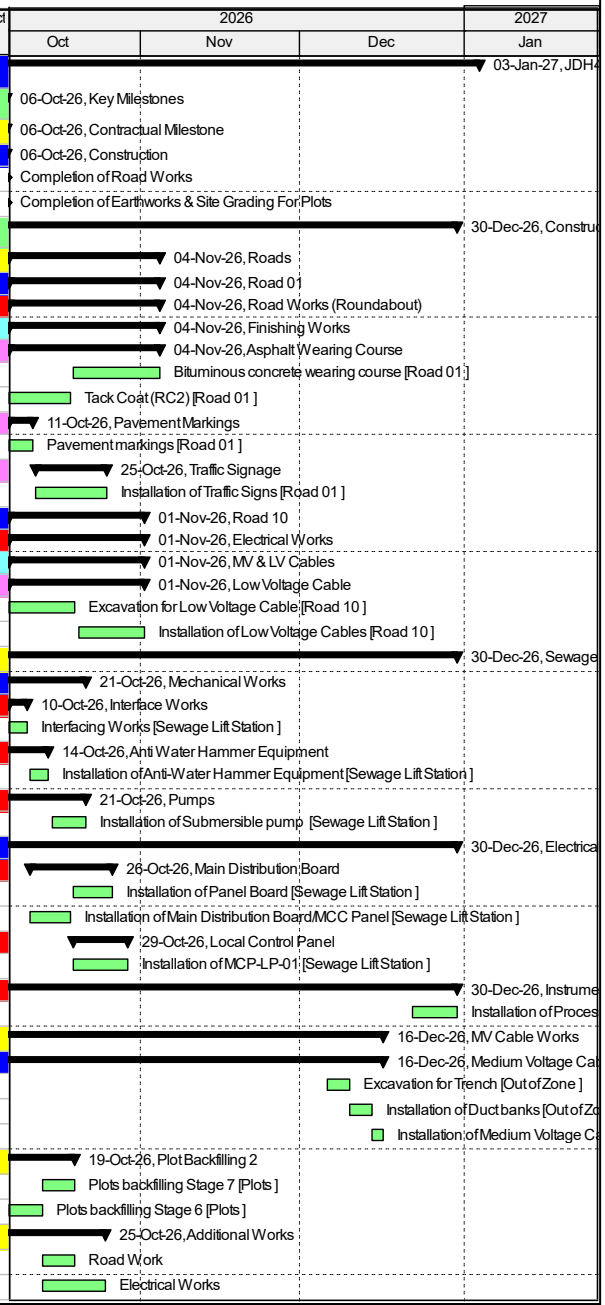

Actual Work | Critical Remaining Work | Remaining Work | Milestone


Date	Revision	Checked	Approved

egis | ENJAZCO شركة الانجاز للتجارة والمقاولات AL Enjaz Company For Trading And Contracting

JDH4-02-007-R-UP-Land Development of Jeddah Oasis- 06 Oct 2026
2 Week Look Ahead

MODON

Activity ID	Activity Name	Original Duration	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Schedule % Complete	Performance % Complete	Variance - BL Project Finish Date
Testing & Commissioning		78	20-Dec-26	05-May-27	09-Jun-26 A	03-Jan-27	0.00	613,975.16	2,455,900.62	0%	25%	101
JDH4-02-007-TC·	Test for Road Works	3	30-Mar-27	01-Apr-27	09-Jun-26 A	22-Nov-26	0.00	327,453.42	818,633.54	0%	40%	108
JDH4-02-007-TC·	Test for Sewage Lift Station	3	03-May-27	05-May-27	17-Jun-26 A	03-Jan-27	0.00	122,795.03	818,633.54	0%	15%	101
JDH4-02-007-TC·	Test for Electrical Network	3	20-Dec-26	22-Dec-26	08-Sep-26 A	22-Nov-26	0.00	163,726.71	818,633.54	0%	20%	26



Actual Work | Critical Remaining Work | Remaining Work | Milestone

Date	Revision	Checked	Approved
