
egis | ENJAZCO شركة الانجاز للتجارة والمقاولات ALEnjaz Company For Trading And Contracting

JDH4-02-007-R-UP-Land Development of Jeddah Oasis- 20 Oct 2026
WBS L5

MODON مدن

Activity ID	Activity Name	Original Duration	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Schedule % Complete	Performance % Complete	Variance - BL Project Finish Date
JDH4-02-007-R-UP-Land Developmen		462	24-Nov-25	23-May-27	24-Nov-25 A	14-Jan-27	35,181,417.75	34,534,354.68	57,304,347.86	61.39%	95.17%	102
Key Milestones		350	24-Nov-25	23-May-27	24-Nov-25 A	14-Jan-27	0.00	0.00	0.00	0%	0%	102
General Milestone		350	24-Nov-25	23-May-27	24-Nov-25 A	14-Jan-27	0.00	0.00	0.00	0%	0%	102
JDH4-02-007-MS	Project Commencement Date	0	24-Nov-25		24-Nov-25 A		0.00	0.00	0.00	100%	100%	0
JDH4-02-007-MS	Project Completion Date	0		23-May-27		14-Jan-27	0.00	0.00	0.00	0%	0%	102
Contractual Milestone		311	23-Dec-25	23-May-27	23-Dec-25 A	30-Dec-26	0.00	0.00	0.00	0%	0%	115
Engineering & Mobilization		185	23-Dec-25	23-Mar-26	23-Dec-25 A	14-Jul-26 A	0.00	0.00	0.00	0%	0%	-94
JDH4-02-007-M	Completion of Mobilization	0		23-Dec-25		23-Dec-25 A	0.00	0.00	0.00	100%	100%	0
JDH4-02-007-M	Submission of the Work Plan (Basel	0		23-Dec-25		23-Dec-25 A	0.00	0.00	0.00	100%	100%	0
JDH4-02-007-M	Submission and Approval of Drawing	0		23-Mar-26		14-Jul-26 A	0.00	0.00	0.00	100%	100%	-94
Construction		61	23-Mar-26	23-May-27	26-Aug-26 A	30-Dec-26	0.00	0.00	0.00	0%	0%	115
JDH4-02-007-M	Completion of Earthworks & Site Gra	0		23-Mar-26		20-Oct-26	0.00	0.00	0.00	100%	0%	-177
JDH4-02-007-M	Completion of Sewerage networks	0		22-Jul-26		26-Aug-26 A	0.00	0.00	0.00	100%	100%	-29
JDH4-02-007-M	Completion of Road Works	0		22-Sep-26		20-Oct-26	0.00	0.00	0.00	100%	0%	-23
JDH4-02-007-M	Completion of Potable Water Netwo	0		23-Nov-26		05-Sep-26 A	0.00	0.00	0.00	0%	100%	68
JDH4-02-007-M	Completion of TSE Network	0		23-Nov-26		30-Aug-26 A	0.00	0.00	0.00	0%	100%	72
JDH4-02-007-M	Completion of Electrical Networks	0		04-Jan-27		19-Nov-26	0.00	0.00	0.00	0%	0%	39
JDH4-02-007-M	Completion of Entire Project	0		23-May-27		30-Dec-26	0.00	0.00	0.00	0%	0%	115
Monitoring & Controlling Milestone		0	14-Oct-26	12-Nov-26	01-Jun-26 A	03-Jun-26 A	0.00	0.00	0.00	0%	0%	138
JDH4-02-007-MS	Approval of Electrical Network Shop	0		14-Oct-26		01-Jun-26 A	0.00	0.00	0.00	100%	100%	115
JDH4-02-007-MS	Approval of Electrical Network Materi	0		12-Nov-26		03-Jun-26 A	0.00	0.00	0.00	0%	100%	138
Mobilization		258	24-Nov-25	29-Sep-26	24-Nov-25 A	01-Jun-26 A	0.00	0.00	0.00	0%	0%	102
Site Facilities & Offices		41	24-Nov-25	10-Jan-26	24-Nov-25 A	10-Jan-26 A	0.00	0.00	0.00	0%	0%	0
JDH4-02-007-MI	Site Layout Plan	5	24-Nov-25	29-Nov-25	24-Nov-25 A	29-Nov-25 A	0.00	0.00	0.00	100%	100%	0
JDH4-02-007-MI	Clear & Grub for Offices & Access Ro	4	30-Nov-25	03-Dec-25	30-Nov-25 A	03-Dec-25 A	0.00	0.00	0.00	100%	100%	0
JDH4-02-007-MI	Construct Site Access Roads	3	30-Nov-25	02-Dec-25	30-Nov-25 A	02-Dec-25 A	0.00	0.00	0.00	100%	100%	0
JDH4-02-007-MI	Construct Temporary Fence	8	04-Dec-25	13-Dec-25	04-Dec-25 A	13-Dec-25 A	0.00	0.00	0.00	100%	100%	0
JDH4-02-007-MI	Construct Site Offices & Storage	17	03-Dec-25	22-Dec-25	03-Dec-25 A	22-Dec-25 A	0.00	0.00	0.00	100%	100%	0
JDH4-02-007-MI	Install Project Signs	15	24-Dec-25	10-Jan-26	24-Dec-25 A	10-Jan-26 A	0.00	0.00	0.00	100%	100%	0
JDH4-02-007-MI	Install Site Facilities	4	14-Dec-25	17-Dec-25	14-Dec-25 A	17-Dec-25 A	0.00	0.00	0.00	100%	100%	0
JDH4-02-007-MI	Electrical Works & Connections	7	14-Dec-25	21-Dec-25	14-Dec-25 A	21-Dec-25 A	0.00	0.00	0.00	100%	100%	0
JDH4-02-007-MI	Construct Parking Sheds	3	31-Dec-25	03-Jan-26	31-Dec-25 A	03-Jan-26 A	0.00	0.00	0.00	100%	100%	0
JDH4-02-007-MI	Mobilization of Equipment	7	15-Dec-25	22-Dec-25	15-Dec-25 A	22-Dec-25 A	0.00	0.00	0.00	100%	100%	0
JDH4-02-007-MI	Mobilization of Manpower	5	18-Dec-25	23-Dec-25	18-Dec-25 A	23-Dec-25 A	0.00	0.00	0.00	100%	100%	0
Topographic Survey		9	24-Nov-25	03-Dec-25	24-Nov-25 A	03-Dec-25 A	0.00	0.00	0.00	0%	0%	0
JDH4-02-007-TF	Site Survey Works	9	24-Nov-25	03-Dec-25	24-Nov-25 A	03-Dec-25 A	0.00	0.00	0.00	100%	100%	0
Permit's and Authority Approvals		258	24-Nov-25	29-Sep-26	24-Nov-25 A	01-Jun-26 A	0.00	0.00	0.00	0%	0%	102
JDH4-02-007-PA	Excavation & Backfilling Permit Perm	20	24-Nov-25	16-Dec-25	24-Nov-25 A	16-Dec-25 A	0.00	0.00	0.00	100%	100%	0
JDH4-02-007-PA	Saudi Electricity Company Permit	20	06-Sep-26	29-Sep-26	03-Feb-26 A	01-Jun-26 A	0.00	0.00	0.00	100%	100%	102
Preliminary Submittals		35	03-Dec-25	12-Jan-26	03-Dec-25 A	12-Jan-26 A	0.00	0.00	0.00	0%	0%	0
Preparation and Submittal by Contractor's		27	03-Dec-25	03-Jan-26	03-Dec-25 A	03-Jan-26 A	0.00	0.00	0.00	0%	0%	0
JDH4-02-007-F	Preparation and Submittal of Detaile	16	03-Dec-25	21-Dec-25	03-Dec-25 A	21-Dec-25 A	0.00	0.00	0.00	100%	100%	0
JDH4-02-007-F	Preparation and Submittal of Project	3	31-Dec-25	03-Jan-26	31-Dec-25 A	03-Jan-26 A	0.00	0.00	0.00	100%	100%	0
JDH4-02-007-F	Preparation and Submittal of Quality	8	03-Dec-25	11-Dec-25	03-Dec-25 A	11-Dec-25 A	0.00	0.00	0.00	100%	100%	0
JDH4-02-007-F	Preparation and Submittal of Safety M	8	03-Dec-25	11-Dec-25	03-Dec-25 A	11-Dec-25 A	0.00	0.00	0.00	100%	100%	0
JDH4-02-007-F	Preparation and Submittal of Organiz	7	03-Dec-25	10-Dec-25	03-Dec-25 A	10-Dec-25 A	0.00	0.00	0.00	100%	100%	0
JDH4-02-007-F	Preparation and Submittal of Comm	7	03-Dec-25	10-Dec-25	03-Dec-25 A	10-Dec-25 A	0.00	0.00	0.00	100%	100%	0
Approval by the Employer's		28	11-Dec-25	12-Jan-26	11-Dec-25 A	12-Jan-26 A	0.00	0.00	0.00	0%	0%	0

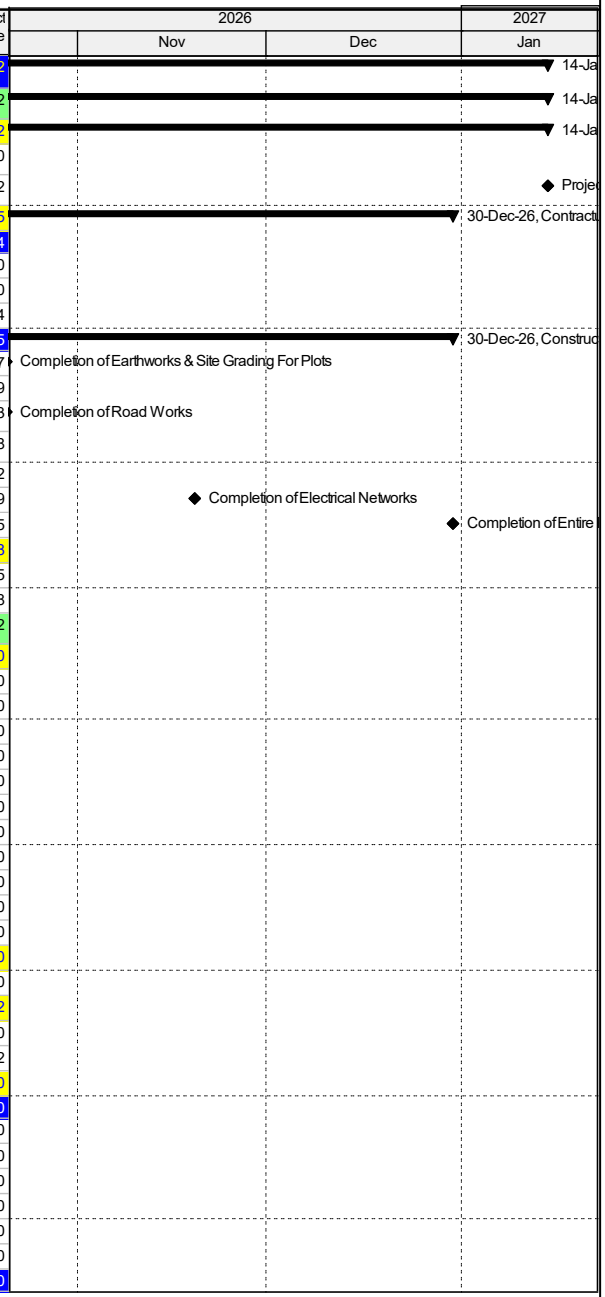

Actual Work | Critical Remaining Work | Remaining Work | Milestone

Date	Revision	Checked	Approved

Activity ID	Activity Name	Original Duration	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Schedule % Complete	Performance % Complete	Variance - BL Project Finish Date
JDH4-02-007-F	Approval of Detailed Work Order Prc	1	21-Dec-25	21-Dec-25	21-Dec-25A	21-Dec-25A	0.00	0.00	0.00	100%	100%	0
JDH4-02-007-F	Approval of Project Execution Plan	1	12-Jan-26	12-Jan-26	12-Jan-26A	12-Jan-26A	0.00	0.00	0.00	100%	100%	0
JDH4-02-007-F	Approval of Quality Management Pla	2	11-Jan-26	12-Jan-26	11-Jan-26A	12-Jan-26A	0.00	0.00	0.00	100%	100%	0
JDH4-02-007-F	Approval of Safety Management Plai	3	31-Dec-25	03-Jan-26	31-Dec-25A	03-Jan-26A	0.00	0.00	0.00	100%	100%	0
JDH4-02-007-F	Approval of Organization Chart	10	11-Dec-25	22-Dec-25	11-Dec-25A	22-Dec-25A	0.00	0.00	0.00	100%	100%	0
JDH4-02-007-F	Approval of Comminumcation Plan	10	11-Dec-25	22-Dec-25	11-Dec-25A	22-Dec-25A	0.00	0.00	0.00	100%	100%	0
Engineering		291	30-Nov-25	12-Nov-26	30-Nov-25A	14-Jul-26A	1,690,947.96	1,719,130.43	1,719,130.43	98.36%	100%	103
Shop Drawings		262	04-Dec-25	14-Oct-26	04-Dec-25A	01-Jun-26A	0.00	0.00	0.00	0%	0%	115
Shop Drawings Submittal		257	04-Dec-25	08-Oct-26	04-Dec-25A	03-Feb-26A	0.00	0.00	0.00	0%	0%	204
Shop Drawings Submittal for Road Works		26	04-Dec-25	03-Jan-26	04-Dec-25A	03-Jan-26A	0.00	0.00	0.00	0%	0%	0
JDH4-02-007-	Shop DWG Submittal for Topograph	8	04-Dec-25	13-Dec-25	04-Dec-25A	13-Dec-25A	0.00	0.00	0.00	100%	100%	0
JDH4-02-007-	Shop DWG Submittal for Road Layc	8	14-Dec-25	22-Dec-25	14-Dec-25A	22-Dec-25A	0.00	0.00	0.00	100%	100%	0
JDH4-02-007-	Shop DWG Submittal for Typical Cro	2	24-Dec-25	25-Dec-25	24-Dec-25A	26-Dec-25A	0.00	0.00	0.00	100%	100%	0
JDH4-02-007-	Shop DWG Submittal for Road Settl	8	14-Dec-25	22-Dec-25	14-Dec-25A	22-Dec-25A	0.00	0.00	0.00	100%	100%	0
JDH4-02-007-	Shop DWG Submittal for Road Profil	8	14-Dec-25	22-Dec-25	14-Dec-25A	22-Dec-25A	0.00	0.00	0.00	100%	100%	0
JDH4-02-007-	Shop DWG Submittal for Grading La	8	14-Dec-25	22-Dec-25	14-Dec-25A	22-Dec-25A	0.00	0.00	0.00	100%	100%	0
JDH4-02-007-	Shop DWG Submittal for Curb Settin	8	14-Dec-25	22-Dec-25	14-Dec-25A	22-Dec-25A	0.00	0.00	0.00	100%	100%	0
JDH4-02-007-	Shop DWG Submittal for Signing & M	3	31-Dec-25	03-Jan-26	31-Dec-25A	03-Jan-26A	0.00	0.00	0.00	100%	100%	0
JDH4-02-007-	Shop DWG Submittal for Standards	8	14-Dec-25	22-Dec-25	14-Dec-25A	22-Dec-25A	0.00	0.00	0.00	100%	100%	0
Shop Drawings Submittal for Stormwater Network		2	04-Jan-26	05-Jan-26	04-Jan-26A	05-Jan-26A	0.00	0.00	0.00	0%	0%	0
JDH4-02-007-	Shop DWG Submittal for Stormwate	2	04-Jan-26	05-Jan-26	04-Jan-26A	05-Jan-26A	0.00	0.00	0.00	100%	100%	0
JDH4-02-007-	Shop DWG Submittal for Stormwate	2	04-Jan-26	05-Jan-26	04-Jan-26A	05-Jan-26A	0.00	0.00	0.00	100%	100%	0
JDH4-02-007-	Shop DWG Submittal for Stormwate	2	04-Jan-26	05-Jan-26	04-Jan-26A	05-Jan-26A	0.00	0.00	0.00	100%	100%	0
Shop Drawings Submittal for Sanitary Sewerage		2	03-Jan-26	04-Jan-26	03-Jan-26A	04-Jan-26A	0.00	0.00	0.00	0%	0%	0
JDH4-02-007-	Shop DWG Submittal for Sanitary Se	2	03-Jan-26	04-Jan-26	03-Jan-26A	04-Jan-26A	0.00	0.00	0.00	100%	100%	0
JDH4-02-007-	Shop DWG Submittal for Sanitary Se	2	03-Jan-26	04-Jan-26	03-Jan-26A	04-Jan-26A	0.00	0.00	0.00	100%	100%	0
JDH4-02-007-	Shop DWG Submittal for Sanitary Se	2	03-Jan-26	04-Jan-26	03-Jan-26A	04-Jan-26A	0.00	0.00	0.00	100%	100%	0
Shop Drawings Submittal for TSE Network		3	01-Jan-26	04-Jan-26	01-Jan-26A	04-Jan-26A	0.00	0.00	0.00	0%	0%	0
JDH4-02-007-	Shop DWG Submittal for TSE Netwc	2	01-Jan-26	03-Jan-26	01-Jan-26A	03-Jan-26A	0.00	0.00	0.00	100%	100%	0
JDH4-02-007-	Shop DWG Submittal for TSE Profile	2	03-Jan-26	04-Jan-26	03-Jan-26A	04-Jan-26A	0.00	0.00	0.00	100%	100%	0
JDH4-02-007-	Shop DWG Submittal for TSE Stand	1	04-Jan-26	04-Jan-26	04-Jan-26A	04-Jan-26A	0.00	0.00	0.00	100%	100%	0
Shop Drawings Submittal for Potable Water Network		4	01-Jan-26	05-Jan-26	01-Jan-26A	05-Jan-26A	0.00	0.00	0.00	0%	0%	0
JDH4-02-007-	Shop DWG Submittal for Potable Wa	4	01-Jan-26	05-Jan-26	01-Jan-26A	05-Jan-26A	0.00	0.00	0.00	100%	100%	0
JDH4-02-007-	Shop DWG Submittal for Potable Wa	4	01-Jan-26	05-Jan-26	01-Jan-26A	05-Jan-26A	0.00	0.00	0.00	100%	100%	0
JDH4-02-007-	Shop DWG Submittal for Potable Wa	4	01-Jan-26	05-Jan-26	01-Jan-26A	05-Jan-26A	0.00	0.00	0.00	100%	100%	0
Shop Drawings Submittal for Electrical Network		232	03-Jan-26	08-Oct-26	03-Jan-26A	03-Feb-26A	0.00	0.00	0.00	0%	0%	204
JDH4-02-007-	Shop DWG Submittal for Medium Vc	8	30-Sep-26	08-Oct-26	01-Feb-26A	03-Feb-26A	0.00	0.00	0.00	100%	100%	204
JDH4-02-007-	Shop DWG Submittal for Street Ligh	3	03-Jan-26	05-Jan-26	03-Jan-26A	05-Jan-26A	0.00	0.00	0.00	100%	100%	0
JDH4-02-007-	Shop DWG Submittal for Low Voltag	3	03-Jan-26	05-Jan-26	03-Jan-26A	05-Jan-26A	0.00	0.00	0.00	100%	100%	0
Shop Drawings Submittal for Telecommunications		2	01-Jan-26	03-Jan-26	01-Jan-26A	03-Jan-26A	0.00	0.00	0.00	0%	0%	0
JDH4-02-007-	Shop DWG Submittal for Telecomm	2	01-Jan-26	03-Jan-26	01-Jan-26A	03-Jan-26A	0.00	0.00	0.00	100%	100%	0
Shop Drawings Submittal for Earthing System		2	01-Jan-26	03-Jan-26	01-Jan-26A	03-Jan-26A	0.00	0.00	0.00	0%	0%	0
JDH4-02-007-	Shop DWG Submittal for Earthing Sy	2	01-Jan-26	03-Jan-26	01-Jan-26A	03-Jan-26A	0.00	0.00	0.00	100%	100%	0
Shop Drawings Submittal for Road Lighting		6	01-Jan-26	07-Jan-26	01-Jan-26A	07-Jan-26A	0.00	0.00	0.00	0%	0%	0
JDH4-02-007-	Shop DWG Submittal for Street Ligh	6	01-Jan-26	07-Jan-26	01-Jan-26A	07-Jan-26A	0.00	0.00	0.00	100%	100%	0
JDH4-02-007-	Shop DWG Submittal for Street Ligh	6	01-Jan-26	07-Jan-26	01-Jan-26A	07-Jan-26A	0.00	0.00	0.00	100%	100%	0
JDH4-02-007-	Shop DWG Submittal for Street Ligh	6	01-Jan-26	07-Jan-26	01-Jan-26A	07-Jan-26A	0.00	0.00	0.00	100%	100%	0
JDH4-02-007-	Shop DWG Submittal for Street Ligh	6	01-Jan-26	07-Jan-26	01-Jan-26A	07-Jan-26A	0.00	0.00	0.00	100%	100%	0
Shop Drawings Submittal for Sewage Lift Station		2	13-Jan-26	14-Jan-26	13-Jan-26A	14-Jan-26A	0.00	0.00	0.00	0%	0%	0
JDH4-02-007-	Shop DWG Submittal for the Sewag	2	13-Jan-26	14-Jan-26	13-Jan-26A	14-Jan-26A	0.00	0.00	0.00	100%	100%	0




Activity ID	Activity Name	Original Duration	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Schedule % Complete	Performance % Complete	Variance - BL Project Finish Date
JDH4-02-007-	Shop DWG Submittal for the Sewag	2	13-Jan-26	14-Jan-26	13-Jan-26A	14-Jan-26A	0.00	0.00	0.00	100%	100%	0
JDH4-02-007-	Shop DWG Submittal for the Sewag	2	13-Jan-26	14-Jan-26	13-Jan-26A	14-Jan-26A	0.00	0.00	0.00	100%	100%	0
JDH4-02-007-	Shop DWG Submittal for the Sewag	2	13-Jan-26	14-Jan-26	13-Jan-26A	14-Jan-26A	0.00	0.00	0.00	100%	100%	0
Shop Drawings Approval		243	27-Dec-25	14-Oct-26	26-Dec-25A	01-Jun-26A	0.00	0.00	0.00	0%	0%	115
Shop Drawings Approval for Road Works		9	27-Dec-25	05-Jan-26	26-Dec-25A	05-Jan-26A	0.00	0.00	0.00	0%	0%	0
JDH4-02-007-	Shop DWG Approval for Topographi	3	27-Dec-25	29-Dec-25	26-Dec-25A	29-Dec-25A	0.00	0.00	0.00	100%	100%	0
JDH4-02-007-	Shop DWG Approval for Road Layo	3	27-Dec-25	29-Dec-25	26-Dec-25A	29-Dec-25A	0.00	0.00	0.00	100%	100%	0
JDH4-02-007-	Shop DWG Approval for Typical Cro	3	27-Dec-25	29-Dec-25	26-Dec-25A	29-Dec-25A	0.00	0.00	0.00	100%	100%	0
JDH4-02-007-	Shop DWG Approval for Road Settir	3	27-Dec-25	29-Dec-25	26-Dec-25A	29-Dec-25A	0.00	0.00	0.00	100%	100%	0
JDH4-02-007-	Shop DWG Approval for Road Profil	3	27-Dec-25	29-Dec-25	26-Dec-25A	29-Dec-25A	0.00	0.00	0.00	100%	100%	0
JDH4-02-007-	Shop DWG Approval for Grading La	3	27-Dec-25	29-Dec-25	26-Dec-25A	29-Dec-25A	0.00	0.00	0.00	100%	100%	0
JDH4-02-007-	Shop DWG Approval for Curb Settin	3	27-Dec-25	29-Dec-25	26-Dec-25A	29-Dec-25A	0.00	0.00	0.00	100%	100%	0
JDH4-02-007-	Shop DWG Approval for Signing & M	3	03-Jan-26	05-Jan-26	03-Jan-26A	05-Jan-26A	0.00	0.00	0.00	100%	100%	0
JDH4-02-007-	Shop DWG Approval for Standards I	3	27-Dec-25	29-Dec-25	26-Dec-25A	29-Dec-25A	0.00	0.00	0.00	100%	100%	0
Shop Drawings Approval for Storm Network		4	08-Jan-26	12-Jan-26	08-Jan-26A	12-Jan-26A	0.00	0.00	0.00	0%	0%	0
JDH4-02-007-	Shop DWG Approval for Stormwater	4	08-Jan-26	12-Jan-26	08-Jan-26A	12-Jan-26A	0.00	0.00	0.00	100%	100%	0
JDH4-02-007-	Shop DWG Approval for Stormwater	4	08-Jan-26	12-Jan-26	08-Jan-26A	12-Jan-26A	0.00	0.00	0.00	100%	100%	0
JDH4-02-007-	Shop DWG Approval for Stormwater	4	08-Jan-26	12-Jan-26	08-Jan-26A	12-Jan-26A	0.00	0.00	0.00	100%	100%	0
Shop Drawings Approval for Sanitary Sewerage		4	08-Jan-26	12-Jan-26	08-Jan-26A	12-Jan-26A	0.00	0.00	0.00	0%	0%	0
JDH4-02-007-	Shop DWG Approval for Sanitary Se	4	08-Jan-26	12-Jan-26	08-Jan-26A	12-Jan-26A	0.00	0.00	0.00	100%	100%	0
JDH4-02-007-	Shop DWG Approval for Sanitary Se	4	08-Jan-26	12-Jan-26	08-Jan-26A	12-Jan-26A	0.00	0.00	0.00	100%	100%	0
JDH4-02-007-	Shop DWG Approval for Sanitary Se	4	08-Jan-26	12-Jan-26	08-Jan-26A	12-Jan-26A	0.00	0.00	0.00	100%	100%	0
Shop Drawings Approval for TSE Network		4	08-Jan-26	12-Jan-26	08-Jan-26A	12-Jan-26A	0.00	0.00	0.00	0%	0%	0
JDH4-02-007-	Shop DWG Approval for TSE Netwo	4	08-Jan-26	12-Jan-26	08-Jan-26A	12-Jan-26A	0.00	0.00	0.00	100%	100%	0
JDH4-02-007-	Shop DWG Approval for TSE Profile	4	08-Jan-26	12-Jan-26	08-Jan-26A	12-Jan-26A	0.00	0.00	0.00	100%	100%	0
JDH4-02-007-	Shop DWG Approval for TSE Standa	4	08-Jan-26	12-Jan-26	08-Jan-26A	12-Jan-26A	0.00	0.00	0.00	100%	100%	0
Shop Drawings Approval for Potable Water Network		4	08-Jan-26	12-Jan-26	08-Jan-26A	12-Jan-26A	0.00	0.00	0.00	0%	0%	0
JDH4-02-007-	Shop DWG Approval for Potable Wa	4	08-Jan-26	12-Jan-26	08-Jan-26A	12-Jan-26A	0.00	0.00	0.00	100%	100%	0
JDH4-02-007-	Shop DWG Approval for Potable Wa	4	08-Jan-26	12-Jan-26	08-Jan-26A	12-Jan-26A	0.00	0.00	0.00	100%	100%	0
JDH4-02-007-	Shop DWG Approval for Potable Wa	4	08-Jan-26	12-Jan-26	08-Jan-26A	12-Jan-26A	0.00	0.00	0.00	100%	100%	0
Shop Drawings Approval for Electrical Network		232	08-Jan-26	14-Oct-26	08-Jan-26A	01-Jun-26A	0.00	0.00	0.00	0%	0%	115
JDH4-02-007-	Shop DWG Approval for Medium Vo	5	10-Oct-26	14-Oct-26	04-Feb-26A	01-Jun-26A	0.00	0.00	0.00	100%	100%	115
JDH4-02-007-	Shop DWG Approval for Street Light	3	08-Jan-26	11-Jan-26	08-Jan-26A	11-Jan-26A	0.00	0.00	0.00	100%	100%	0
JDH4-02-007-	Shop DWG Approval for Low Voltag	3	08-Jan-26	11-Jan-26	08-Jan-26A	11-Jan-26A	0.00	0.00	0.00	100%	100%	0
Shop Drawings Approval for Telecommunications		2	03-Jan-26	04-Jan-26	03-Jan-26A	04-Jan-26A	0.00	0.00	0.00	0%	0%	0
JDH4-02-007-	Shop DWG Approval for Telecommu	2	03-Jan-26	04-Jan-26	03-Jan-26A	04-Jan-26A	0.00	0.00	0.00	100%	100%	0
Shop Drawings Approval for Earthing System		2	10-Jan-26	11-Jan-26	10-Jan-26A	11-Jan-26A	0.00	0.00	0.00	0%	0%	0
JDH4-02-007-	Shop DWG Approval for Earthing Sy	2	10-Jan-26	11-Jan-26	10-Jan-26A	11-Jan-26A	0.00	0.00	0.00	100%	100%	0
Shop Drawings Approval for Road Lighting		5	10-Jan-26	14-Jan-26	10-Jan-26A	14-Jan-26A	0.00	0.00	0.00	0%	0%	0
JDH4-02-007-	Shop DWG Approval for Street Light	5	10-Jan-26	14-Jan-26	10-Jan-26A	14-Jan-26A	0.00	0.00	0.00	100%	100%	0
JDH4-02-007-	Shop DWG Approval for Street Light	5	10-Jan-26	14-Jan-26	10-Jan-26A	14-Jan-26A	0.00	0.00	0.00	100%	100%	0
JDH4-02-007-	Shop DWG Approval for Street Light	5	10-Jan-26	14-Jan-26	10-Jan-26A	14-Jan-26A	0.00	0.00	0.00	100%	100%	0
JDH4-02-007-	Shop DWG Approval for Street Light	5	10-Jan-26	14-Jan-26	10-Jan-26A	14-Jan-26A	0.00	0.00	0.00	100%	100%	0
Shop Drawings Approval for Sewage Lift Station		3	08-Jan-26	11-Jan-26	08-Jan-26A	11-Jan-26A	0.00	0.00	0.00	0%	0%	0
JDH4-02-007-	Shop DWG Approval for the Sewage	3	08-Jan-26	11-Jan-26	08-Jan-26A	11-Jan-26A	0.00	0.00	0.00	100%	100%	0
JDH4-02-007-	Shop DWG Approval for the Sewage	3	08-Jan-26	11-Jan-26	08-Jan-26A	11-Jan-26A	0.00	0.00	0.00	100%	100%	0
JDH4-02-007-	Shop DWG Approval for the Sewage	3	08-Jan-26	11-Jan-26	08-Jan-26A	11-Jan-26A	0.00	0.00	0.00	100%	100%	0
JDH4-02-007-	Shop DWG Approval for the Sewage	3	08-Jan-26	11-Jan-26	08-Jan-26A	11-Jan-26A	0.00	0.00	0.00	100%	100%	0
Method Statements		32	30-Nov-25	05-Jan-26	30-Nov-25A	05-Jan-26A	0.00	0.00	0.00	0%	0%	0
Method Statements Submittal		30	30-Nov-25	03-Jan-26	30-Nov-25A	03-Jan-26A	0.00	0.00	0.00	0%	0%	0

2026 | 2027

Nov | Dec | Jan


Date	Revision	Checked	Approved

Activity ID	Activity Name	Original Duration	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Schedule % Complete	Performance % Complete	Variance - BL Project Finish Date
JDH4-02-007-E	Preparation & Submission of Methoc	8	30-Nov-25	08-Dec-25	30-Nov-25A	08-Dec-25A	0.00	0.00	0.00	100%	100%	0
JDH4-02-007-E	Preparation & Submission of Methoc	8	30-Nov-25	08-Dec-25	30-Nov-25A	08-Dec-25A	0.00	0.00	0.00	100%	100%	0
JDH4-02-007-E	Preparation & Submission of Methoc	15	30-Nov-25	16-Dec-25	30-Nov-25A	16-Dec-25A	0.00	0.00	0.00	100%	100%	0
JDH4-02-007-E	Preparation & Submission of Methoc	3	31-Dec-25	03-Jan-26	31-Dec-25A	03-Jan-26A	0.00	0.00	0.00	100%	100%	0
Method Statements Approval		24	09-Dec-25	05-Jan-26	09-Dec-25A	05-Jan-26A	0.00	0.00	0.00	0%	0%	0
JDH4-02-007-E	Approval of Method Statement for Ea	7	09-Dec-25	16-Dec-25	09-Dec-25A	16-Dec-25A	0.00	0.00	0.00	100%	100%	0
JDH4-02-007-E	Approval of Method Statement for Cc	8	09-Dec-25	17-Dec-25	09-Dec-25A	17-Dec-25A	0.00	0.00	0.00	100%	100%	0
JDH4-02-007-E	Approval of Method Statement for W	5	17-Dec-25	22-Dec-25	17-Dec-25A	22-Dec-25A	0.00	0.00	0.00	100%	100%	0
JDH4-02-007-E	Approval of Method Statement for As	3	03-Jan-26	05-Jan-26	03-Jan-26A	05-Jan-26A	0.00	0.00	0.00	100%	100%	0
Method Statements Staging Time		17	17-Dec-25	05-Jan-26	17-Dec-25A	05-Jan-26A	0.00	0.00	0.00	0%	0%	0
JDH4-02-007-E	Staging Time of Method Statement fo	6	17-Dec-25	23-Dec-25	17-Dec-25A	23-Dec-25A	0.00	0.00	0.00	100%	100%	0
JDH4-02-007-E	Staging Time of Method Statement fo	4	18-Dec-25	22-Dec-25	18-Dec-25A	22-Dec-25A	0.00	0.00	0.00	100%	100%	0
JDH4-02-007-E	Staging Time of Method Statement fo	5	31-Dec-25	05-Jan-26	31-Dec-25A	05-Jan-26A	0.00	0.00	0.00	100%	100%	0
JDH4-02-007-E	Staging Time of Method Statement fo	2	04-Jan-26	05-Jan-26	04-Jan-26A	05-Jan-26A	0.00	0.00	0.00	100%	100%	0
Pre-qualification and Material		287	04-Dec-25	12-Nov-26	04-Dec-25A	14-Jul-26A	1,690,947.96	1,719,130.43	1,719,130.43	98.36%	100%	103
Pre-qualification		212	04-Dec-25	26-Oct-26	04-Dec-25A	09-Jun-26A	0.00	0.00	0.00	0%	0%	118
Road Works - Civil		28	04-Dec-25	05-Jan-26	04-Dec-25A	05-Jan-26A	0.00	0.00	0.00	0%	0%	0
Steel Reinforcement		11	04-Dec-25	16-Dec-25	04-Dec-25A	16-Dec-25A	0.00	0.00	0.00	0%	0%	0
JDH4-02-007	Pre-Qualification Submittal for Steel F	5	04-Dec-25	09-Dec-25	04-Dec-25A	09-Dec-25A	0.00	0.00	0.00	100%	100%	0
JDH4-02-007	Pre-Qualification Approval for Steel R	6	10-Dec-25	16-Dec-25	10-Dec-25A	16-Dec-25A	0.00	0.00	0.00	100%	100%	0
Ready Mixed Concrete		11	10-Dec-25	22-Dec-25	10-Dec-25A	22-Dec-25A	0.00	0.00	0.00	0%	0%	0
JDH4-02-007	Pre-Qualification Submittal for Ready	5	10-Dec-25	15-Dec-25	10-Dec-25A	15-Dec-25A	0.00	0.00	0.00	100%	100%	0
JDH4-02-007	Pre-Qualification Approval for Ready	6	16-Dec-25	22-Dec-25	16-Dec-25A	22-Dec-25A	0.00	0.00	0.00	100%	100%	0
Water Proofing		6	16-Dec-25	22-Dec-25	16-Dec-25A	22-Dec-25A	0.00	0.00	0.00	0%	0%	0
JDH4-02-007	Pre-Qualification Submittal for Water	5	16-Dec-25	21-Dec-25	16-Dec-25A	21-Dec-25A	0.00	0.00	0.00	100%	100%	0
JDH4-02-007	Pre-Qualification Approval for Water I	1	22-Dec-25	22-Dec-25	22-Dec-25A	22-Dec-25A	0.00	0.00	0.00	100%	100%	0
Aggregate Base Course		6	16-Dec-25	22-Dec-25	16-Dec-25A	22-Dec-25A	0.00	0.00	0.00	0%	0%	0
JDH4-02-007	Pre-Qualification Submittal for Aggre	4	16-Dec-25	20-Dec-25	16-Dec-25A	20-Dec-25A	0.00	0.00	0.00	100%	100%	0
JDH4-02-007	Pre-Qualification Approval for Aggre	2	21-Dec-25	22-Dec-25	21-Dec-25A	22-Dec-25A	0.00	0.00	0.00	100%	100%	0
Bituminous Base & Wearing Course		4	24-Dec-25	28-Dec-25	24-Dec-25A	28-Dec-25A	0.00	0.00	0.00	0%	0%	0
JDH4-02-007	Pre-Qualification Submittal for Bitumi	4	24-Dec-25	28-Dec-25	24-Dec-25A	28-Dec-25A	0.00	0.00	0.00	100%	100%	0
JDH4-02-007	Pre-Qualification Approval for Bitumir	2	27-Dec-25	28-Dec-25	26-Dec-25A	28-Dec-25A	0.00	0.00	0.00	100%	100%	0
Precast Concrete Kerb		4	18-Dec-25	22-Dec-25	18-Dec-25A	22-Dec-25A	0.00	0.00	0.00	0%	0%	0
JDH4-02-007	Pre-Qualification Submittal for Precas	4	18-Dec-25	22-Dec-25	18-Dec-25A	22-Dec-25A	0.00	0.00	0.00	100%	100%	0
JDH4-02-007	Pre-Qualification Approval for Precas	4	18-Dec-25	22-Dec-25	18-Dec-25A	22-Dec-25A	0.00	0.00	0.00	100%	100%	0
Interlocking Block Pavers		9	22-Dec-25	31-Dec-25	22-Dec-25A	31-Dec-25A	0.00	0.00	0.00	0%	0%	0
JDH4-02-007	Pre-Qualification Submittal for Interloc	9	22-Dec-25	31-Dec-25	22-Dec-25A	31-Dec-25A	0.00	0.00	0.00	100%	100%	0
JDH4-02-007	Pre-Qualification Approval for Interloc	1	22-Dec-25	22-Dec-25	22-Dec-25A	22-Dec-25A	0.00	0.00	0.00	100%	100%	0
Pavement Markings		13	22-Dec-25	05-Jan-26	22-Dec-25A	05-Jan-26A	0.00	0.00	0.00	0%	0%	0
JDH4-02-007	Pre-Qualification Submittal for Paven	9	22-Dec-25	31-Dec-25	22-Dec-25A	31-Dec-25A	0.00	0.00	0.00	100%	100%	0
JDH4-02-007	Pre-Qualification Approval for Paver	3	03-Jan-26	05-Jan-26	03-Jan-26A	05-Jan-26A	0.00	0.00	0.00	100%	100%	0
Traffic Signs		13	22-Dec-25	05-Jan-26	22-Dec-25A	05-Jan-26A	0.00	0.00	0.00	0%	0%	0
JDH4-02-007	Pre-Qualification Submittal for Traffic S	9	22-Dec-25	31-Dec-25	22-Dec-25A	31-Dec-25A	0.00	0.00	0.00	100%	100%	0
JDH4-02-007	Pre-Qualification Approval for Traffic S	3	03-Jan-26	05-Jan-26	03-Jan-26A	05-Jan-26A	0.00	0.00	0.00	100%	100%	0
Storm Network		24	04-Dec-25	31-Dec-25	04-Dec-25A	31-Dec-25A	0.00	0.00	0.00	0%	0%	0
GRP Pipes		24	04-Dec-25	31-Dec-25	04-Dec-25A	31-Dec-25A	0.00	0.00	0.00	0%	0%	0
JDH4-02-007	Pre-Qualification Submittal for GRP F	24	04-Dec-25	31-Dec-25	04-Dec-25A	31-Dec-25A	0.00	0.00	0.00	100%	100%	0
JDH4-02-007	Pre-Qualification Approval for GRP P	6	09-Dec-25	15-Dec-25	09-Dec-25A	15-Dec-25A	0.00	0.00	0.00	100%	100%	0
Catch Basin		24	04-Dec-25	31-Dec-25	04-Dec-25A	31-Dec-25A	0.00	0.00	0.00	0%	0%	0
JDH4-02-007	Pre-Qualification Submittal for Catch	24	04-Dec-25	31-Dec-25	04-Dec-25A	31-Dec-25A	0.00	0.00	0.00	100%	100%	0
JDH4-02-007	Pre-Qualification Approval for Catch I	6	09-Dec-25	15-Dec-25	09-Dec-25A	15-Dec-25A	0.00	0.00	0.00	100%	100%	0

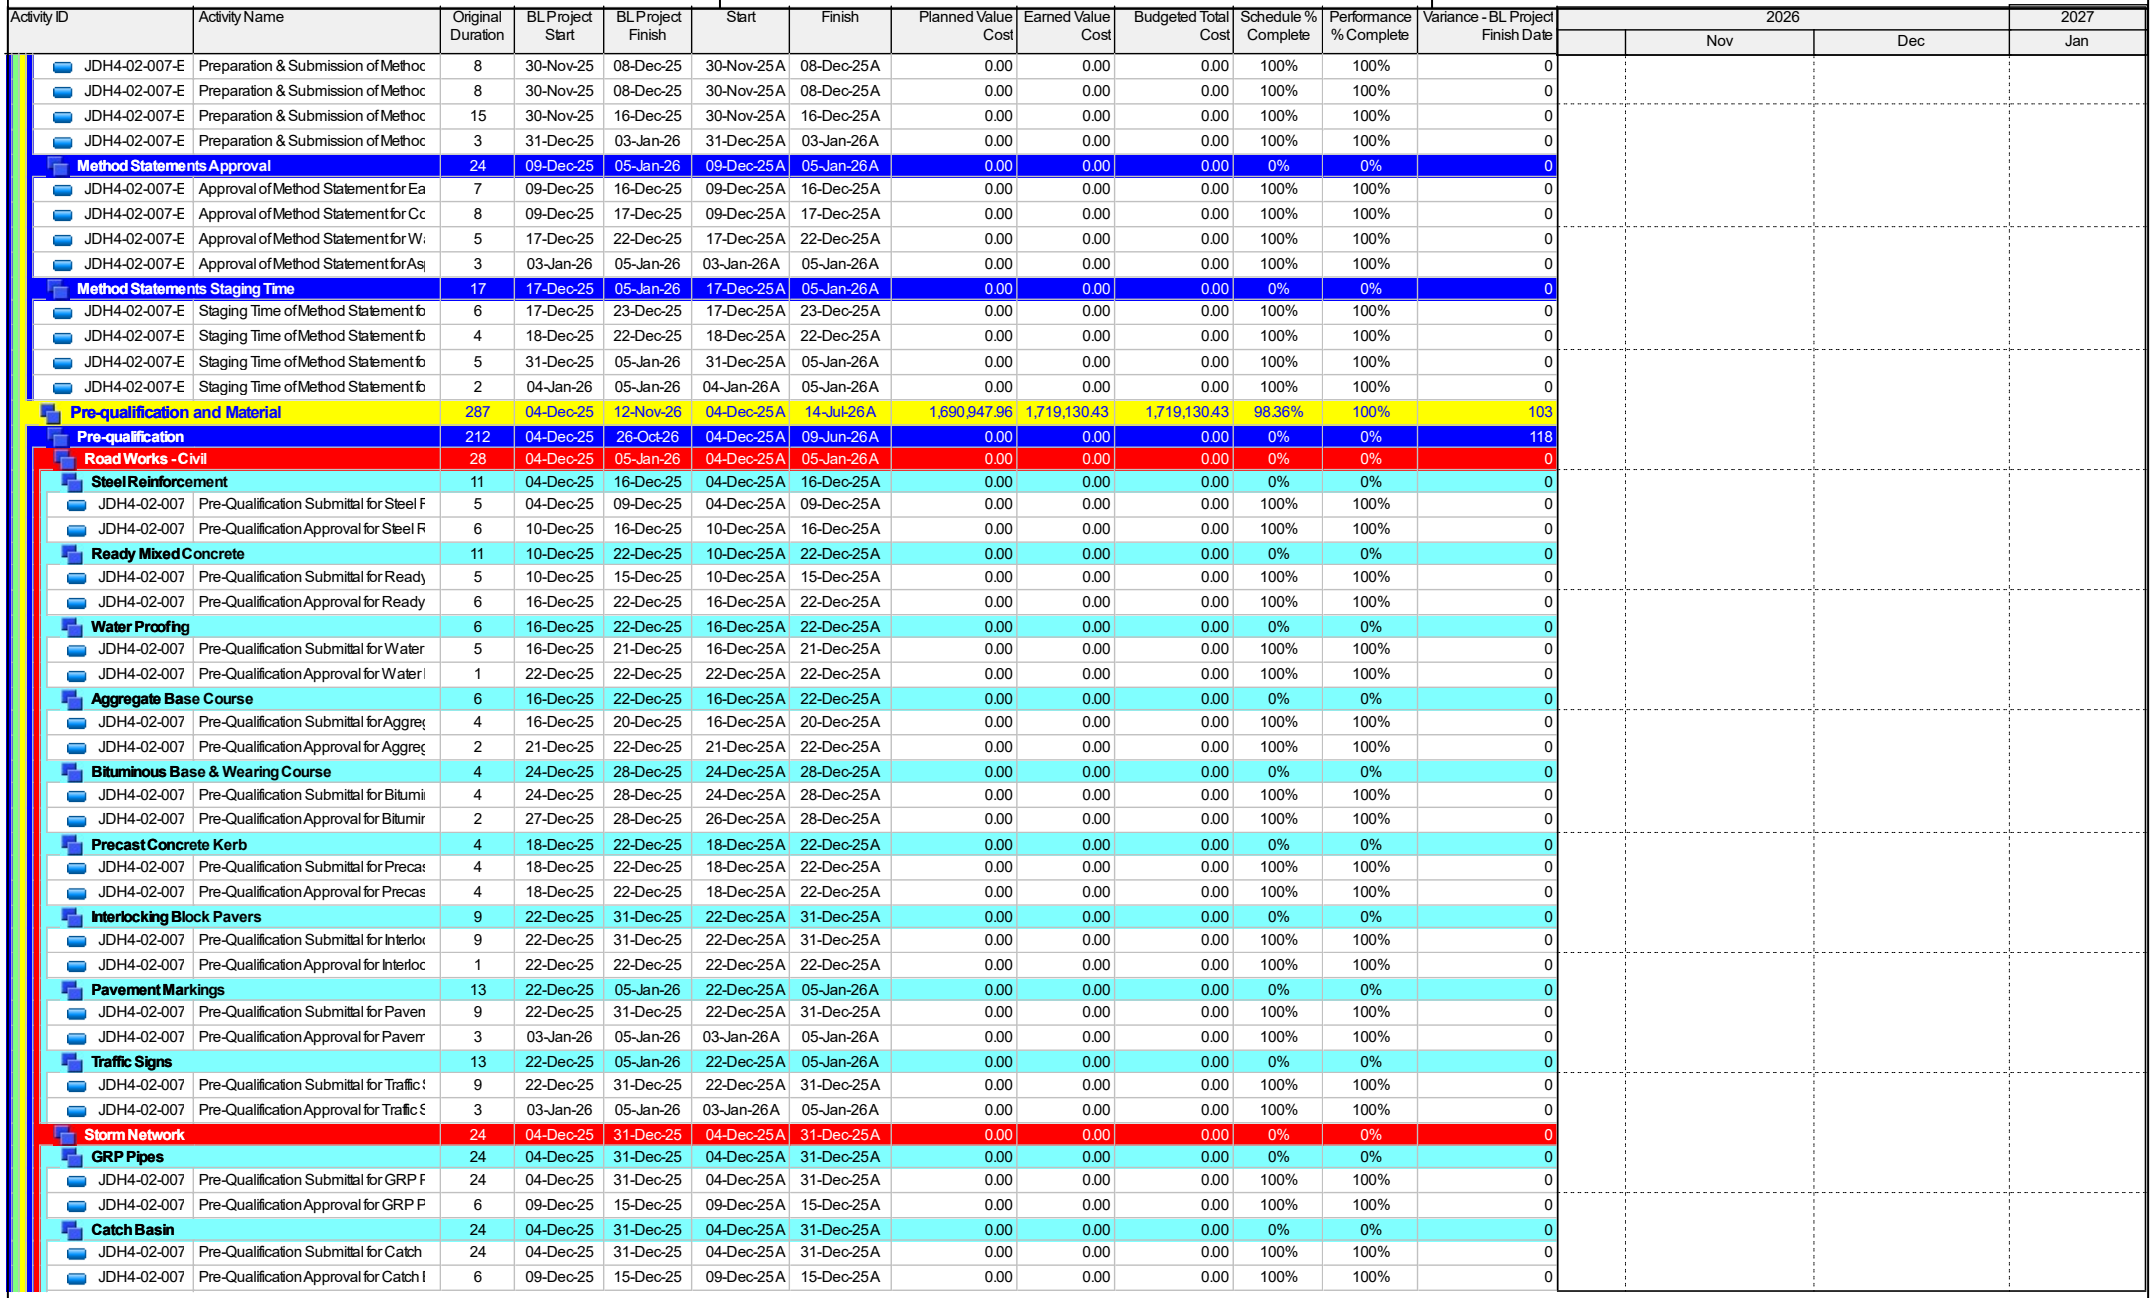


Date	Revision	Checked	Approved

Activity ID	Activity Name	Original Duration	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Schedule % Complete	Performance % Complete	Variance - BL Project Finish Date
Inlet Manholes		20	09-Dec-25	31-Dec-25	09-Dec-25A	31-Dec-25A	0.00	0.00	0.00	0%	0%	0
JDH4-02-007	Pre-Qualification Submittal for Inlet M	20	09-Dec-25	31-Dec-25	09-Dec-25A	31-Dec-25A	0.00	0.00	0.00	100%	100%	0
JDH4-02-007	Pre-Qualification Approval for Inlet Ma	6	14-Dec-25	20-Dec-25	14-Dec-25A	20-Dec-25A	0.00	0.00	0.00	100%	100%	0
Sanitary Sewerage		24	04-Dec-25	31-Dec-25	04-Dec-25A	31-Dec-25A	0.00	0.00	0.00	0%	0%	0
GRP Pipes		24	04-Dec-25	31-Dec-25	04-Dec-25A	31-Dec-25A	0.00	0.00	0.00	0%	0%	0
JDH4-02-007	Pre-Qualification Submittal for GRP F	24	04-Dec-25	31-Dec-25	04-Dec-25A	31-Dec-25A	0.00	0.00	0.00	100%	100%	0
JDH4-02-007	Pre-Qualification Approval for GRP P	6	08-Dec-25	14-Dec-25	08-Dec-25A	14-Dec-25A	0.00	0.00	0.00	100%	100%	0
Manholes		21	08-Dec-25	31-Dec-25	08-Dec-25A	31-Dec-25A	0.00	0.00	0.00	0%	0%	0
JDH4-02-007	Pre-Qualification Submittal for Manho	21	08-Dec-25	31-Dec-25	08-Dec-25A	31-Dec-25A	0.00	0.00	0.00	100%	100%	0
JDH4-02-007	Pre-Qualification Approval for Manho	6	11-Dec-25	17-Dec-25	11-Dec-25A	17-Dec-25A	0.00	0.00	0.00	100%	100%	0
TSE Network		24	04-Dec-25	31-Dec-25	04-Dec-25A	31-Dec-25A	0.00	0.00	0.00	0%	0%	0
HDPE Pipe (PN 16)		24	04-Dec-25	31-Dec-25	04-Dec-25A	31-Dec-25A	0.00	0.00	0.00	0%	0%	0
JDH4-02-007	Pre-Qualification Submittal for HDPE	24	04-Dec-25	31-Dec-25	04-Dec-25A	31-Dec-25A	0.00	0.00	0.00	100%	100%	0
JDH4-02-007	Pre-Qualification Approval for HDPE	6	08-Dec-25	14-Dec-25	08-Dec-25A	14-Dec-25A	0.00	0.00	0.00	100%	100%	0
Valves / Chambers		21	08-Dec-25	31-Dec-25	08-Dec-25A	31-Dec-25A	0.00	0.00	0.00	0%	0%	0
JDH4-02-007	Pre-Qualification Submittal for Valves	21	08-Dec-25	31-Dec-25	08-Dec-25A	31-Dec-25A	0.00	0.00	0.00	100%	100%	0
JDH4-02-007	Pre-Qualification Approval for Valves	6	11-Dec-25	17-Dec-25	11-Dec-25A	17-Dec-25A	0.00	0.00	0.00	100%	100%	0
Risers		18	11-Dec-25	31-Dec-25	11-Dec-25A	31-Dec-25A	0.00	0.00	0.00	0%	0%	0
JDH4-02-007	Pre-Qualification Submittal for Risers	18	11-Dec-25	31-Dec-25	11-Dec-25A	31-Dec-25A	0.00	0.00	0.00	100%	100%	0
JDH4-02-007	Pre-Qualification Approval for Risers	6	16-Dec-25	22-Dec-25	16-Dec-25A	22-Dec-25A	0.00	0.00	0.00	100%	100%	0
Potable Water Network		24	04-Dec-25	31-Dec-25	04-Dec-25A	31-Dec-25A	0.00	0.00	0.00	0%	0%	0
HDPE Pipe (PN 16)		24	04-Dec-25	31-Dec-25	04-Dec-25A	31-Dec-25A	0.00	0.00	0.00	0%	0%	0
JDH4-02-007	Pre-Qualification Submittal for HDPE	24	04-Dec-25	31-Dec-25	04-Dec-25A	31-Dec-25A	0.00	0.00	0.00	100%	100%	0
JDH4-02-007	Pre-Qualification Approval for HDPE	6	09-Dec-25	15-Dec-25	09-Dec-25A	15-Dec-25A	0.00	0.00	0.00	100%	100%	0
Valves / Chambers		20	09-Dec-25	31-Dec-25	09-Dec-25A	31-Dec-25A	0.00	0.00	0.00	0%	0%	0
JDH4-02-007	Pre-Qualification Submittal for Valves	20	09-Dec-25	31-Dec-25	09-Dec-25A	31-Dec-25A	0.00	0.00	0.00	100%	100%	0
JDH4-02-007	Pre-Qualification Approval for Valves	6	14-Dec-25	20-Dec-25	14-Dec-25A	20-Dec-25A	0.00	0.00	0.00	100%	100%	0
Fire Hydrant		18	11-Dec-25	31-Dec-25	11-Dec-25A	31-Dec-25A	0.00	0.00	0.00	0%	0%	0
JDH4-02-007	Pre-Qualification Submittal for Fire Hy	18	11-Dec-25	31-Dec-25	11-Dec-25A	31-Dec-25A	0.00	0.00	0.00	100%	100%	0
JDH4-02-007	Pre-Qualification Approval for Fire Hy	5	15-Dec-25	20-Dec-25	15-Dec-25A	20-Dec-25A	0.00	0.00	0.00	100%	100%	0
Electrical Network		197	22-Dec-25	26-Oct-26	22-Dec-25A	09-Jun-26A	0.00	0.00	0.00	0%	0%	118
Pipe for the Duct		9	22-Dec-25	31-Dec-25	22-Dec-25A	31-Dec-25A	0.00	0.00	0.00	0%	0%	0
JDH4-02-007	Pre-Qualification Submittal for Pipe fo	9	22-Dec-25	31-Dec-25	22-Dec-25A	31-Dec-25A	0.00	0.00	0.00	100%	100%	0
JDH4-02-007	Pre-Qualification Approval for Pipe fo	1	29-Dec-25	29-Dec-25	29-Dec-25A	29-Dec-25A	0.00	0.00	0.00	100%	100%	0
Low Voltage Cables		13	22-Dec-25	05-Jan-26	22-Dec-25A	05-Jan-26A	0.00	0.00	0.00	0%	0%	0
JDH4-02-007	Pre-Qualification Submittal for Low Vo	9	22-Dec-25	31-Dec-25	22-Dec-25A	31-Dec-25A	0.00	0.00	0.00	100%	100%	0
JDH4-02-007	Pre-Qualification Approval for Low Vo	3	03-Jan-26	05-Jan-26	03-Jan-26A	05-Jan-26A	0.00	0.00	0.00	100%	100%	0
Earthing System		13	22-Dec-25	05-Jan-26	22-Dec-25A	05-Jan-26A	0.00	0.00	0.00	0%	0%	0
JDH4-02-007	Pre-Qualification Submittal for Earthir	9	22-Dec-25	31-Dec-25	22-Dec-25A	31-Dec-25A	0.00	0.00	0.00	100%	100%	0
JDH4-02-007	Pre-Qualification Approval for Earthin	3	03-Jan-26	05-Jan-26	03-Jan-26A	05-Jan-26A	0.00	0.00	0.00	100%	100%	0
Medium Voltage Cable		10	15-Oct-26	26-Oct-26	06-Jun-26A	09-Jun-26A	0.00	0.00	0.00	0%	0%	118
JDH4-02-007	Pre-Qualification Submittal for Mediur	7	15-Oct-26	22-Oct-26	06-Jun-26A	06-Jun-26A	0.00	0.00	0.00	71.43%	100%	118
JDH4-02-007	Pre-Qualification Approval for Mediur	3	24-Oct-26	26-Oct-26	07-Jun-26A	09-Jun-26A	0.00	0.00	0.00	0%	100%	118
Low Voltage Distribution Panel		25	22-Dec-25	19-Jan-26	22-Dec-25A	19-Jan-26A	0.00	0.00	0.00	0%	0%	0
JDH4-02-007	Pre-Qualification Submittal for Low Vo	9	22-Dec-25	31-Dec-25	22-Dec-25A	31-Dec-25A	0.00	0.00	0.00	100%	100%	0
JDH4-02-007	Pre-Qualification Approval for Low Vo	15	03-Jan-26	19-Jan-26	03-Jan-26A	19-Jan-26A	0.00	0.00	0.00	100%	100%	0
Unit Sub Station		13	22-Dec-25	05-Jan-26	22-Dec-25A	05-Jan-26A	0.00	0.00	0.00	0%	0%	0
JDH4-02-007	Pre-Qualification Submittal for Unit Su	9	22-Dec-25	31-Dec-25	22-Dec-25A	31-Dec-25A	0.00	0.00	0.00	100%	100%	0
JDH4-02-007	Pre-Qualification Approval for Unit Su	3	03-Jan-26	05-Jan-26	03-Jan-26A	05-Jan-26A	0.00	0.00	0.00	100%	100%	0
Ring Main Unit (RMU)		13	22-Dec-25	05-Jan-26	22-Dec-25A	05-Jan-26A	0.00	0.00	0.00	0%	0%	0
JDH4-02-007	Pre-Qualification Submittal for Ring n	9	22-Dec-25	31-Dec-25	22-Dec-25A	31-Dec-25A	0.00	0.00	0.00	100%	100%	0

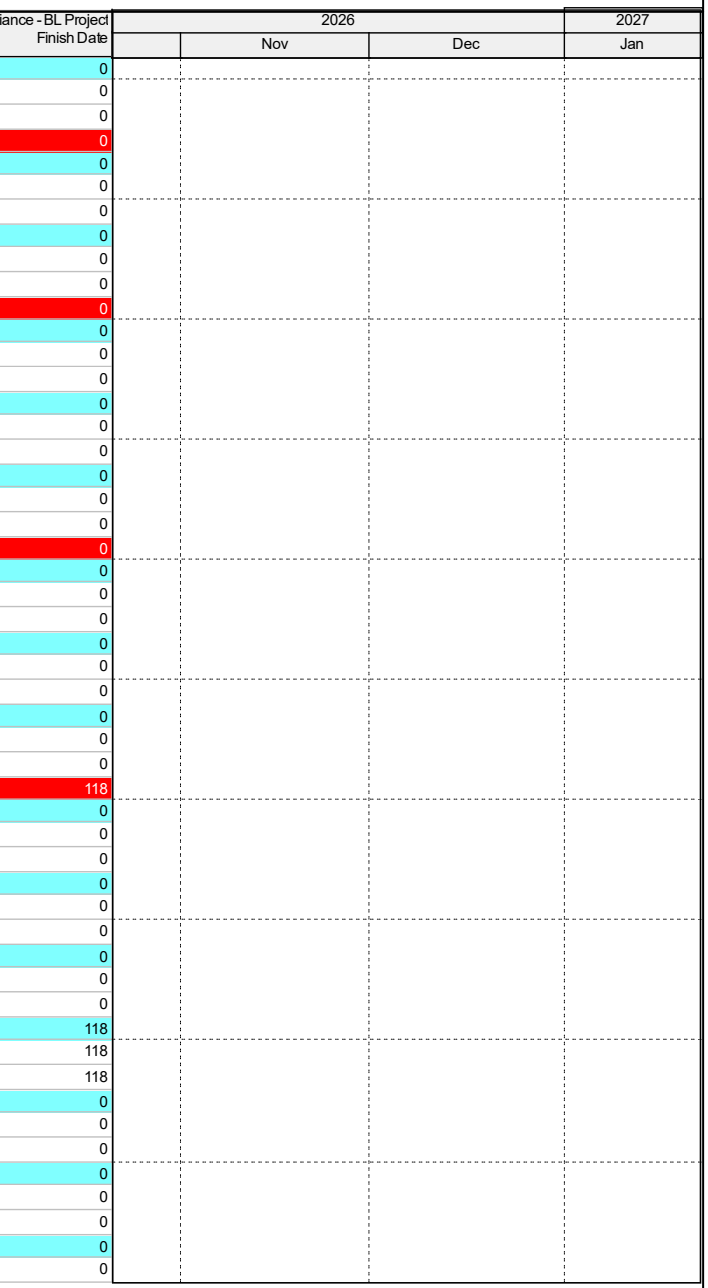


Date	Revision	Checked	Approved

Activity ID	Activity Name	Original Duration	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Schedule % Complete	Performance % Complete	Variance - BL Project Finish Date
JDH4-02-007	Pre-Qualification Approval for Ring m	3	03-Jan-26	05-Jan-26	03-Jan-26 A	05-Jan-26 A	0.00	0.00	0.00	100%	100%	0
Lighting poles		13	22-Dec-25	05-Jan-26	22-Dec-25 A	05-Jan-26 A	0.00	0.00	0.00	0%	0%	0
JDH4-02-007	Pre-Qualification Submittal for Lightin	9	22-Dec-25	31-Dec-25	22-Dec-25 A	31-Dec-25 A	0.00	0.00	0.00	100%	100%	0
JDH4-02-007	Pre-Qualification Approval for Lightin	3	03-Jan-26	05-Jan-26	03-Jan-26 A	05-Jan-26 A	0.00	0.00	0.00	100%	100%	0
Lighting panels/Feeder Pillers		13	22-Dec-25	05-Jan-26	22-Dec-25 A	05-Jan-26 A	0.00	0.00	0.00	0%	0%	0
JDH4-02-007	Pre-Qualification Submittal for Lightin	9	22-Dec-25	31-Dec-25	22-Dec-25 A	31-Dec-25 A	0.00	0.00	0.00	100%	100%	0
JDH4-02-007	Pre-Qualification Approval for Lightin	3	03-Jan-26	05-Jan-26	03-Jan-26 A	05-Jan-26 A	0.00	0.00	0.00	100%	100%	0
Street Lighting Luminaire		13	22-Dec-25	05-Jan-26	22-Dec-25 A	05-Jan-26 A	0.00	0.00	0.00	0%	0%	0
JDH4-02-007	Pre-Qualification Submittal for Street	9	22-Dec-25	31-Dec-25	22-Dec-25 A	31-Dec-25 A	0.00	0.00	0.00	100%	100%	0
JDH4-02-007	Pre-Qualification Approval for Street L	3	03-Jan-26	05-Jan-26	03-Jan-26 A	05-Jan-26 A	0.00	0.00	0.00	100%	100%	0
Telecommunications		11	20-Dec-25	31-Dec-25	20-Dec-25 A	31-Dec-25 A	0.00	0.00	0.00	0%	0%	0
Pipe for the Duct		11	20-Dec-25	31-Dec-25	20-Dec-25 A	31-Dec-25 A	0.00	0.00	0.00	0%	0%	0
JDH4-02-007	Pre-Qualification Submittal for Pipe fo	9	22-Dec-25	31-Dec-25	22-Dec-25 A	31-Dec-25 A	0.00	0.00	0.00	100%	100%	0
JDH4-02-007	Pre-Qualification Approval for Pipe fo	3	20-Dec-25	22-Dec-25	20-Dec-25 A	22-Dec-25 A	0.00	0.00	0.00	100%	100%	0
Sewage Lift Station		13	22-Dec-25	05-Jan-26	22-Dec-25 A	05-Jan-26 A	0.00	0.00	0.00	0%	0%	0
Thermal & Moisture Protection		13	22-Dec-25	05-Jan-26	22-Dec-25 A	05-Jan-26 A	0.00	0.00	0.00	0%	0%	0
JDH4-02-007	Pre-Qualification Submittal for Therm	9	22-Dec-25	31-Dec-25	22-Dec-25 A	31-Dec-25 A	0.00	0.00	0.00	100%	100%	0
JDH4-02-007	Pre-Qualification Approval for Therm	3	03-Jan-26	05-Jan-26	03-Jan-26 A	05-Jan-26 A	0.00	0.00	0.00	100%	100%	0
Metals		13	22-Dec-25	05-Jan-26	22-Dec-25 A	05-Jan-26 A	0.00	0.00	0.00	0%	0%	0
JDH4-02-007	Pre-Qualification Submittal for Metal	9	22-Dec-25	31-Dec-25	22-Dec-25 A	31-Dec-25 A	0.00	0.00	0.00	100%	100%	0
JDH4-02-007	Pre-Qualification Approval for Metal	3	03-Jan-26	05-Jan-26	03-Jan-26 A	05-Jan-26 A	0.00	0.00	0.00	100%	100%	0
Pumps		13	22-Dec-25	05-Jan-26	22-Dec-25 A	05-Jan-26 A	0.00	0.00	0.00	0%	0%	0
JDH4-02-007	Pre-Qualification Submittal for pumps	9	22-Dec-25	31-Dec-25	22-Dec-25 A	31-Dec-25 A	0.00	0.00	0.00	100%	100%	0
JDH4-02-007	Pre-Qualification Approval for pumps	3	03-Jan-26	05-Jan-26	03-Jan-26 A	05-Jan-26 A	0.00	0.00	0.00	100%	100%	0
Pipes,Fittings & Valves		13	22-Dec-25	05-Jan-26	22-Dec-25 A	05-Jan-26 A	0.00	0.00	0.00	0%	0%	0
JDH4-02-007	Pre-Qualification Submittal for Pipes,	9	22-Dec-25	31-Dec-25	22-Dec-25 A	31-Dec-25 A	0.00	0.00	0.00	100%	100%	0
JDH4-02-007	Pre-Qualification Approval for Pipes,F	3	03-Jan-26	05-Jan-26	03-Jan-26 A	05-Jan-26 A	0.00	0.00	0.00	100%	100%	0
Odours scrubbing system		13	22-Dec-25	05-Jan-26	22-Dec-25 A	05-Jan-26 A	0.00	0.00	0.00	0%	0%	0
JDH4-02-007	Pre-Qualification Submittal for Odour	9	22-Dec-25	31-Dec-25	22-Dec-25 A	31-Dec-25 A	0.00	0.00	0.00	100%	100%	0
JDH4-02-007	Pre-Qualification Approval for Odours	3	03-Jan-26	05-Jan-26	03-Jan-26 A	05-Jan-26 A	0.00	0.00	0.00	100%	100%	0
Crane		13	22-Dec-25	05-Jan-26	22-Dec-25 A	05-Jan-26 A	0.00	0.00	0.00	0%	0%	0
JDH4-02-007	Pre-Qualification Submittal for Crane	9	22-Dec-25	31-Dec-25	22-Dec-25 A	31-Dec-25 A	0.00	0.00	0.00	100%	100%	0
JDH4-02-007	Pre-Qualification Approval for Crane	3	03-Jan-26	05-Jan-26	03-Jan-26 A	05-Jan-26 A	0.00	0.00	0.00	100%	100%	0
Air Vents		13	22-Dec-25	05-Jan-26	22-Dec-25 A	05-Jan-26 A	0.00	0.00	0.00	0%	0%	0
JDH4-02-007	Pre-Qualification Submittal for Air Ver	9	22-Dec-25	31-Dec-25	22-Dec-25 A	31-Dec-25 A	0.00	0.00	0.00	100%	100%	0
JDH4-02-007	Pre-Qualification Approval for Air Ven	3	03-Jan-26	05-Jan-26	03-Jan-26 A	05-Jan-26 A	0.00	0.00	0.00	100%	100%	0
Screening Container		13	22-Dec-25	05-Jan-26	22-Dec-25 A	05-Jan-26 A	0.00	0.00	0.00	0%	0%	0
JDH4-02-007	Pre-Qualification Submittal for Screer	9	22-Dec-25	31-Dec-25	22-Dec-25 A	31-Dec-25 A	0.00	0.00	0.00	100%	100%	0
JDH4-02-007	Pre-Qualification Approval for Screer	3	03-Jan-26	05-Jan-26	03-Jan-26 A	05-Jan-26 A	0.00	0.00	0.00	100%	100%	0
Baffle Plates		13	22-Dec-25	05-Jan-26	22-Dec-25 A	05-Jan-26 A	0.00	0.00	0.00	0%	0%	0
JDH4-02-007	Pre-Qualification Submittal for Baffle	9	22-Dec-25	31-Dec-25	22-Dec-25 A	31-Dec-25 A	0.00	0.00	0.00	100%	100%	0
JDH4-02-007	Pre-Qualification Approval for Baffle	3	03-Jan-26	05-Jan-26	03-Jan-26 A	05-Jan-26 A	0.00	0.00	0.00	100%	100%	0
Anti-Water Hammer Equipment		13	22-Dec-25	05-Jan-26	22-Dec-25 A	05-Jan-26 A	0.00	0.00	0.00	0%	0%	0
JDH4-02-007	Pre-Qualification Submittal for Anti-W	9	22-Dec-25	31-Dec-25	22-Dec-25 A	31-Dec-25 A	0.00	0.00	0.00	100%	100%	0
JDH4-02-007	Pre-Qualification Approval for Anti-W	3	03-Jan-26	05-Jan-26	03-Jan-26 A	05-Jan-26 A	0.00	0.00	0.00	100%	100%	0
Air Conditioning and Ventilation		13	22-Dec-25	05-Jan-26	22-Dec-25 A	05-Jan-26 A	0.00	0.00	0.00	0%	0%	0
JDH4-02-007	Pre-Qualification Submittal for Air Co	9	22-Dec-25	31-Dec-25	22-Dec-25 A	31-Dec-25 A	0.00	0.00	0.00	100%	100%	0
JDH4-02-007	Pre-Qualification Approval for Air Cor	3	03-Jan-26	05-Jan-26	03-Jan-26 A	05-Jan-26 A	0.00	0.00	0.00	100%	100%	0
Fuel System		13	22-Dec-25	05-Jan-26	22-Dec-25 A	05-Jan-26 A	0.00	0.00	0.00	0%	0%	0
JDH4-02-007	Pre-Qualification Submittal for Fuel S	9	22-Dec-25	31-Dec-25	22-Dec-25 A	31-Dec-25 A	0.00	0.00	0.00	100%	100%	0
JDH4-02-007	Pre-Qualification Approval for Fuel Sy	3	03-Jan-26	05-Jan-26	03-Jan-26 A	05-Jan-26 A	0.00	0.00	0.00	100%	100%	0

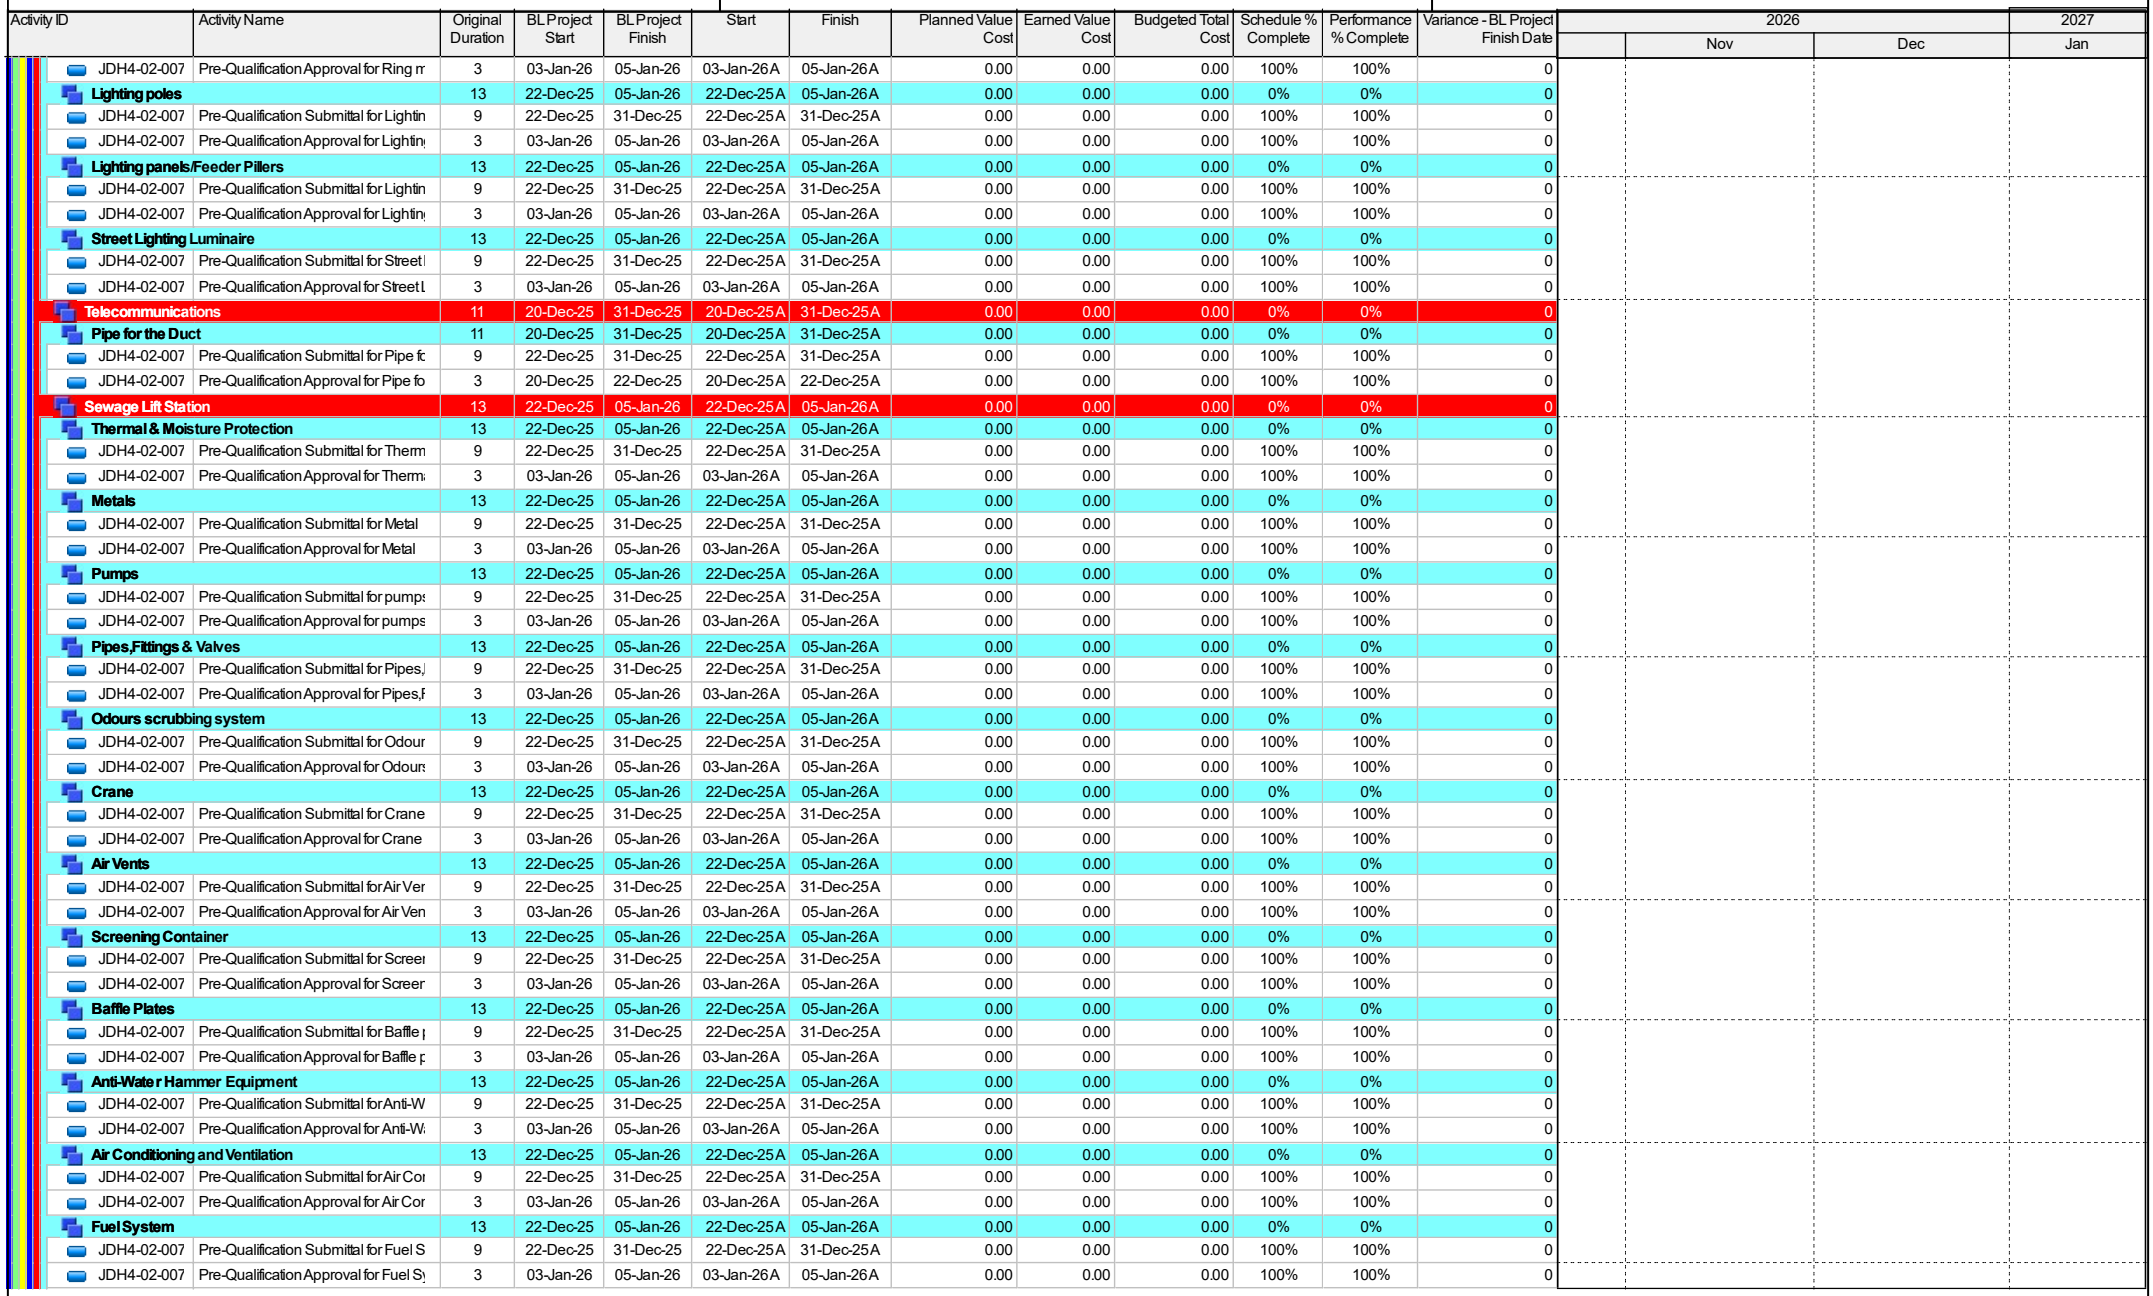


Date	Revision	Checked	Approved

Activity ID	Activity Name	Original Duration	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Schedule % Complete	Performance % Complete	Variance - BL Project Finish Date
Fire Fighting System		13	22-Dec-25	05-Jan-26	22-Dec-25A	05-Jan-26A	0.00	0.00	0.00	0%	0%	0
JDH4-02-007	Pre-Qualification Submittal for Fire Fig	9	22-Dec-25	31-Dec-25	22-Dec-25A	31-Dec-25A	0.00	0.00	0.00	100%	100%	0
JDH4-02-007	Pre-Qualification Approval for Fire Fig	3	03-Jan-26	05-Jan-26	03-Jan-26A	05-Jan-26A	0.00	0.00	0.00	100%	100%	0
Main Distribution Board /MCC panels		13	22-Dec-25	05-Jan-26	22-Dec-25A	05-Jan-26A	0.00	0.00	0.00	0%	0%	0
JDH4-02-007	Pre-Qualification Submittal for Main D	9	22-Dec-25	31-Dec-25	22-Dec-25A	31-Dec-25A	0.00	0.00	0.00	100%	100%	0
JDH4-02-007	Pre-Qualification Approval for Main D	3	03-Jan-26	05-Jan-26	03-Jan-26A	05-Jan-26A	0.00	0.00	0.00	100%	100%	0
Final Panel boards		13	22-Dec-25	05-Jan-26	22-Dec-25A	05-Jan-26A	0.00	0.00	0.00	0%	0%	0
JDH4-02-007	Pre-Qualification Submittal for Final P	9	22-Dec-25	31-Dec-25	22-Dec-25A	31-Dec-25A	0.00	0.00	0.00	100%	100%	0
JDH4-02-007	Pre-Qualification Approval for Final P	3	03-Jan-26	05-Jan-26	03-Jan-26A	05-Jan-26A	0.00	0.00	0.00	100%	100%	0
Local Control Panel/ Monitoring Control Panel		13	22-Dec-25	05-Jan-26	22-Dec-25A	05-Jan-26A	0.00	0.00	0.00	0%	0%	0
JDH4-02-007	Pre-Qualification Submittal for Local (	9	22-Dec-25	31-Dec-25	22-Dec-25A	31-Dec-25A	0.00	0.00	0.00	100%	100%	0
JDH4-02-007	Pre-Qualification Approval for Local (	3	03-Jan-26	05-Jan-26	03-Jan-26A	05-Jan-26A	0.00	0.00	0.00	100%	100%	0
Engine Generators		13	22-Dec-25	05-Jan-26	22-Dec-25A	05-Jan-26A	0.00	0.00	0.00	0%	0%	0
JDH4-02-007	Pre-Qualification Submittal for Engine	9	22-Dec-25	31-Dec-25	22-Dec-25A	31-Dec-25A	0.00	0.00	0.00	100%	100%	0
JDH4-02-007	Pre-Qualification Approval for Engine	3	03-Jan-26	05-Jan-26	03-Jan-26A	05-Jan-26A	0.00	0.00	0.00	100%	100%	0
Standby Diesel Generator		13	22-Dec-25	05-Jan-26	22-Dec-25A	05-Jan-26A	0.00	0.00	0.00	0%	0%	0
JDH4-02-007	Pre-Qualification Submittal for Standl	9	22-Dec-25	31-Dec-25	22-Dec-25A	31-Dec-25A	0.00	0.00	0.00	100%	100%	0
JDH4-02-007	Pre-Qualification Approval for Standl	3	03-Jan-26	05-Jan-26	03-Jan-26A	05-Jan-26A	0.00	0.00	0.00	100%	100%	0
Power Factor Correction Capacitor Bank		13	22-Dec-25	05-Jan-26	22-Dec-25A	05-Jan-26A	0.00	0.00	0.00	0%	0%	0
JDH4-02-007	Pre-Qualification Submittal for Power	9	22-Dec-25	31-Dec-25	22-Dec-25A	31-Dec-25A	0.00	0.00	0.00	100%	100%	0
JDH4-02-007	Pre-Qualification Approval for Power	3	03-Jan-26	05-Jan-26	03-Jan-26A	05-Jan-26A	0.00	0.00	0.00	100%	100%	0
Low-Voltage Electrical Power Conductors and Cab		13	22-Dec-25	05-Jan-26	22-Dec-25A	05-Jan-26A	0.00	0.00	0.00	0%	0%	0
JDH4-02-007	Pre-Qualification Submittal for Low Vo	9	22-Dec-25	31-Dec-25	22-Dec-25A	31-Dec-25A	0.00	0.00	0.00	100%	100%	0
JDH4-02-007	Pre-Qualification Approval for Low Vo	3	03-Jan-26	05-Jan-26	03-Jan-26A	05-Jan-26A	0.00	0.00	0.00	100%	100%	0
Low Voltage Feeder Cable		13	22-Dec-25	05-Jan-26	22-Dec-25A	05-Jan-26A	0.00	0.00	0.00	0%	0%	0
JDH4-02-007	Pre-Qualification Submittal for Low Vo	9	22-Dec-25	31-Dec-25	22-Dec-25A	31-Dec-25A	0.00	0.00	0.00	100%	100%	0
JDH4-02-007	Pre-Qualification Approval for Low Vo	3	03-Jan-26	05-Jan-26	03-Jan-26A	05-Jan-26A	0.00	0.00	0.00	100%	100%	0
Wiring Devices		13	22-Dec-25	05-Jan-26	22-Dec-25A	05-Jan-26A	0.00	0.00	0.00	0%	0%	0
JDH4-02-007	Pre-Qualification Submittal for Wiring	9	22-Dec-25	31-Dec-25	22-Dec-25A	31-Dec-25A	0.00	0.00	0.00	100%	100%	0
JDH4-02-007	Pre-Qualification Approval for Wiring	3	03-Jan-26	05-Jan-26	03-Jan-26A	05-Jan-26A	0.00	0.00	0.00	100%	100%	0
Enclosed Switches and Circuit Breakers		13	22-Dec-25	05-Jan-26	22-Dec-25A	05-Jan-26A	0.00	0.00	0.00	0%	0%	0
JDH4-02-007	Pre-Qualification Submittal for Enclos	9	22-Dec-25	31-Dec-25	22-Dec-25A	31-Dec-25A	0.00	0.00	0.00	100%	100%	0
JDH4-02-007	Pre-Qualification Approval for Enclos	3	03-Jan-26	05-Jan-26	03-Jan-26A	05-Jan-26A	0.00	0.00	0.00	100%	100%	0
Raceways for Electrical Systems		13	22-Dec-25	05-Jan-26	22-Dec-25A	05-Jan-26A	0.00	0.00	0.00	0%	0%	0
JDH4-02-007	Pre-Qualification Submittal for Racev	9	22-Dec-25	31-Dec-25	22-Dec-25A	31-Dec-25A	0.00	0.00	0.00	100%	100%	0
JDH4-02-007	Pre-Qualification Approval for Racew	3	03-Jan-26	05-Jan-26	03-Jan-26A	05-Jan-26A	0.00	0.00	0.00	100%	100%	0
Electrical Manholes		13	22-Dec-25	05-Jan-26	22-Dec-25A	05-Jan-26A	0.00	0.00	0.00	0%	0%	0
JDH4-02-007	Pre-Qualification Submittal for Electric	9	22-Dec-25	31-Dec-25	22-Dec-25A	31-Dec-25A	0.00	0.00	0.00	100%	100%	0
JDH4-02-007	Pre-Qualification Approval for Electric	3	03-Jan-26	05-Jan-26	03-Jan-26A	05-Jan-26A	0.00	0.00	0.00	100%	100%	0
Security System (CCTV System)		13	22-Dec-25	05-Jan-26	22-Dec-25A	05-Jan-26A	0.00	0.00	0.00	0%	0%	0
JDH4-02-007	Pre-Qualification Submittal for Securi	9	22-Dec-25	31-Dec-25	22-Dec-25A	31-Dec-25A	0.00	0.00	0.00	100%	100%	0
JDH4-02-007	Pre-Qualification Approval for Securit	3	03-Jan-26	05-Jan-26	03-Jan-26A	05-Jan-26A	0.00	0.00	0.00	100%	100%	0
ICT (Data& telephone System)		13	22-Dec-25	05-Jan-26	22-Dec-25A	05-Jan-26A	0.00	0.00	0.00	0%	0%	0
JDH4-02-007	Pre-Qualification Submittal for ICT (D	9	22-Dec-25	31-Dec-25	22-Dec-25A	31-Dec-25A	0.00	0.00	0.00	100%	100%	0
JDH4-02-007	Pre-Qualification Approval for ICT (Da	3	03-Jan-26	05-Jan-26	03-Jan-26A	05-Jan-26A	0.00	0.00	0.00	100%	100%	0
Programmable Logic Controllers		13	22-Dec-25	05-Jan-26	22-Dec-25A	05-Jan-26A	0.00	0.00	0.00	0%	0%	0
JDH4-02-007	Pre-Qualification Submittal for Progra	9	22-Dec-25	31-Dec-25	22-Dec-25A	31-Dec-25A	0.00	0.00	0.00	100%	100%	0
JDH4-02-007	Pre-Qualification Approval for Progra	3	03-Jan-26	05-Jan-26	03-Jan-26A	05-Jan-26A	0.00	0.00	0.00	100%	100%	0
Process Control Wiring		13	22-Dec-25	05-Jan-26	22-Dec-25A	05-Jan-26A	0.00	0.00	0.00	0%	0%	0
JDH4-02-007	Pre-Qualification Submittal for Proces	9	22-Dec-25	31-Dec-25	22-Dec-25A	31-Dec-25A	0.00	0.00	0.00	100%	100%	0
JDH4-02-007	Pre-Qualification Approval for Proces	3	03-Jan-26	05-Jan-26	03-Jan-26A	05-Jan-26A	0.00	0.00	0.00	100%	100%	0

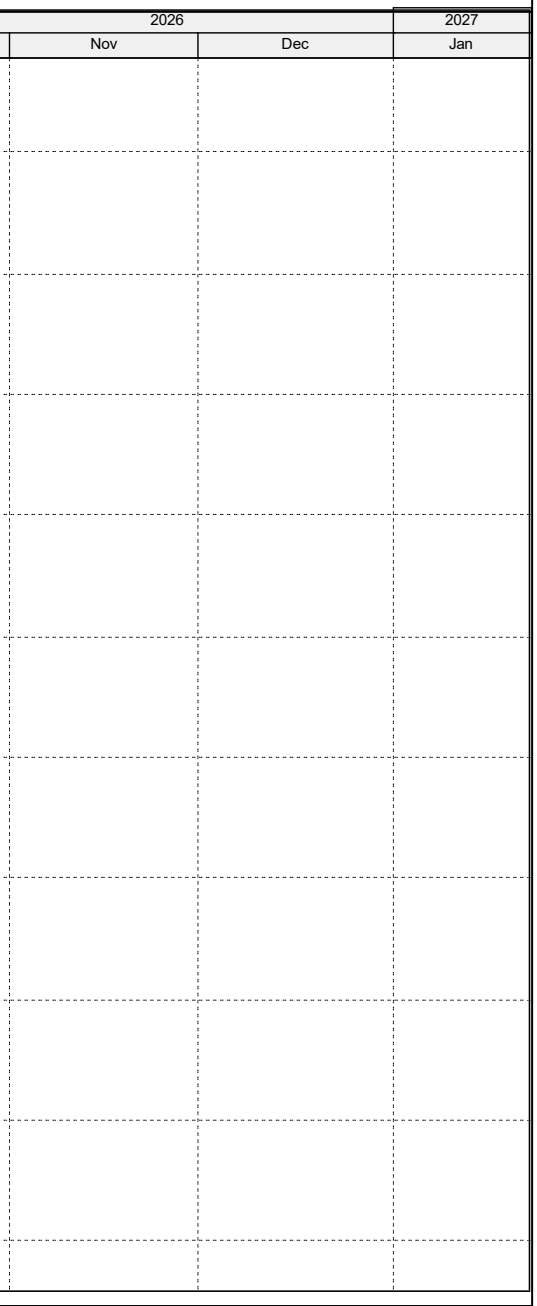


Date	Revision	Checked	Approved

Activity ID	Activity Name	Original Duration	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Schedule % Complete	Performance % Complete	Variance - BL Project Finish Date
Instrumentation for Process Systems		13	22-Dec-25	05-Jan-26	22-Dec-25A	05-Jan-26A	0.00	0.00	0.00	0%	0%	0
JDH4-02-007	Pre-Qualification Submittal for Instrun	9	22-Dec-25	31-Dec-25	22-Dec-25A	31-Dec-25A	0.00	0.00	0.00	100%	100%	0
JDH4-02-007	Pre-Qualification Approval for Instrum	3	03-Jan-26	05-Jan-26	03-Jan-26A	05-Jan-26A	0.00	0.00	0.00	100%	100%	0
Material Submittal & Approval		270	24-Dec-25	12-Nov-26	24-Dec-25A	14-Jul-26A	1,690,947.96	1,719,130.43	1,719,130.43	98.36%	100%	103
Road Works - Civil		16	24-Dec-25	11-Jan-26	24-Dec-25A	11-Jan-26A	253,642.23	253,642.23	253,642.23	100%	100%	0
Steel Reinforcement		5	24-Dec-25	29-Dec-25	24-Dec-25A	29-Dec-25A	28,182.47	28,182.47	28,182.47	100%	100%	0
JDH4-02-007	Material Submittal for Steel Reinforce	5	24-Dec-25	29-Dec-25	24-Dec-25A	29-Dec-25A	0.00	0.00	0.00	100%	100%	0
JDH4-02-007	Material Approval for Steel Reinforcei	5	24-Dec-25	29-Dec-25	24-Dec-25A	29-Dec-25A	28,182.47	28,182.47	28,182.47	100%	100%	0
Ready Mixed Concrete		5	24-Dec-25	29-Dec-25	24-Dec-25A	29-Dec-25A	28,182.47	28,182.47	28,182.47	100%	100%	0
JDH4-02-007	Material Submittal for Ready Mixed C	5	24-Dec-25	29-Dec-25	24-Dec-25A	29-Dec-25A	0.00	0.00	0.00	100%	100%	0
JDH4-02-007	Material Approval for Ready Mixed C	5	24-Dec-25	29-Dec-25	24-Dec-25A	29-Dec-25A	28,182.47	28,182.47	28,182.47	100%	100%	0
Water Proofing		5	24-Dec-25	29-Dec-25	24-Dec-25A	29-Dec-25A	28,182.47	28,182.47	28,182.47	100%	100%	0
JDH4-02-007	Material Submittal for Water Proofing	5	24-Dec-25	29-Dec-25	24-Dec-25A	29-Dec-25A	0.00	0.00	0.00	100%	100%	0
JDH4-02-007	Material Approval for Water Proofing	5	24-Dec-25	29-Dec-25	24-Dec-25A	29-Dec-25A	28,182.47	28,182.47	28,182.47	100%	100%	0
Aggregate Base Course		5	24-Dec-25	29-Dec-25	24-Dec-25A	29-Dec-25A	28,182.47	28,182.47	28,182.47	100%	100%	0
JDH4-02-007	Material Submittal for Aggregate Bas	5	24-Dec-25	29-Dec-25	24-Dec-25A	29-Dec-25A	0.00	0.00	0.00	100%	100%	0
JDH4-02-007	Material Approval for Aggregate Base	5	24-Dec-25	29-Dec-25	24-Dec-25A	29-Dec-25A	28,182.47	28,182.47	28,182.47	100%	100%	0
Bituminous Base & Wearing Course		5	24-Dec-25	29-Dec-25	24-Dec-25A	29-Dec-25A	28,182.47	28,182.47	28,182.47	100%	100%	0
JDH4-02-007	Material Submittal for Bituminous Bas	5	24-Dec-25	29-Dec-25	24-Dec-25A	29-Dec-25A	0.00	0.00	0.00	100%	100%	0
JDH4-02-007	Material Approval for Bituminous & W	5	24-Dec-25	29-Dec-25	24-Dec-25A	29-Dec-25A	28,182.47	28,182.47	28,182.47	100%	100%	0
Precast Concrete Kerb		4	07-Jan-26	11-Jan-26	07-Jan-26A	11-Jan-26A	28,182.47	28,182.47	28,182.47	100%	100%	0
JDH4-02-007	Material Submittal for Precast Concre	2	07-Jan-26	08-Jan-26	07-Jan-26A	08-Jan-26A	0.00	0.00	0.00	100%	100%	0
JDH4-02-007	Material Approval for Precast Concre	2	10-Jan-26	11-Jan-26	10-Jan-26A	11-Jan-26A	28,182.47	28,182.47	28,182.47	100%	100%	0
Interlocking Block Pavers		4	07-Jan-26	11-Jan-26	07-Jan-26A	11-Jan-26A	28,182.47	28,182.47	28,182.47	100%	100%	0
JDH4-02-007	Material Submittal for Interlocking Blo	2	07-Jan-26	08-Jan-26	07-Jan-26A	08-Jan-26A	0.00	0.00	0.00	100%	100%	0
JDH4-02-007	Material Approval for Interlocking Bloc	2	10-Jan-26	11-Jan-26	10-Jan-26A	11-Jan-26A	28,182.47	28,182.47	28,182.47	100%	100%	0
Pavement Markings		4	07-Jan-26	11-Jan-26	07-Jan-26A	11-Jan-26A	28,182.47	28,182.47	28,182.47	100%	100%	0
JDH4-02-007	Material Submittal for Pavement Marl	2	07-Jan-26	08-Jan-26	07-Jan-26A	08-Jan-26A	0.00	0.00	0.00	100%	100%	0
JDH4-02-007	Material Approval for Pavement Mark	2	10-Jan-26	11-Jan-26	10-Jan-26A	11-Jan-26A	28,182.47	28,182.47	28,182.47	100%	100%	0
Traffic Signs		4	07-Jan-26	11-Jan-26	07-Jan-26A	11-Jan-26A	28,182.47	28,182.47	28,182.47	100%	100%	0
JDH4-02-007	Material Submittal for Traffic Signs	2	07-Jan-26	08-Jan-26	07-Jan-26A	08-Jan-26A	0.00	0.00	0.00	100%	100%	0
JDH4-02-007	Material Approval for Trafic Signs	2	10-Jan-26	11-Jan-26	10-Jan-26A	11-Jan-26A	28,182.47	28,182.47	28,182.47	100%	100%	0
Storm Network		5	24-Dec-25	29-Dec-25	24-Dec-25A	29-Dec-25A	84,547.41	84,547.41	84,547.41	100%	100%	0
GRP Pipes		5	24-Dec-25	29-Dec-25	24-Dec-25A	29-Dec-25A	28,182.47	28,182.47	28,182.47	100%	100%	0
JDH4-02-007	Material Submittal for GRP Pipe	5	24-Dec-25	29-Dec-25	24-Dec-25A	29-Dec-25A	0.00	0.00	0.00	100%	100%	0
JDH4-02-007	Material Approval for GRP Pipe	5	24-Dec-25	29-Dec-25	24-Dec-25A	29-Dec-25A	28,182.47	28,182.47	28,182.47	100%	100%	0
Catch Basin		5	24-Dec-25	29-Dec-25	24-Dec-25A	29-Dec-25A	28,182.47	28,182.47	28,182.47	100%	100%	0
JDH4-02-007	Material Submittal for Catch Basin	5	24-Dec-25	29-Dec-25	24-Dec-25A	29-Dec-25A	0.00	0.00	0.00	100%	100%	0
JDH4-02-007	Material Approval for Catch Basin	5	24-Dec-25	29-Dec-25	24-Dec-25A	29-Dec-25A	28,182.47	28,182.47	28,182.47	100%	100%	0
Inlet Manholes		5	24-Dec-25	29-Dec-25	24-Dec-25A	29-Dec-25A	28,182.47	28,182.47	28,182.47	100%	100%	0
JDH4-02-007	Material Submittal for Inlet Manholes	5	24-Dec-25	29-Dec-25	24-Dec-25A	29-Dec-25A	0.00	0.00	0.00	100%	100%	0
JDH4-02-007	Material Approval for Inlet Manholes	5	24-Dec-25	29-Dec-25	24-Dec-25A	29-Dec-25A	28,182.47	28,182.47	28,182.47	100%	100%	0
Sanitary Sewerage		5	24-Dec-25	29-Dec-25	24-Dec-25A	29-Dec-25A	56,364.94	56,364.94	56,364.94	100%	100%	0
GRP Pipes		5	24-Dec-25	29-Dec-25	24-Dec-25A	29-Dec-25A	28,182.47	28,182.47	28,182.47	100%	100%	0
JDH4-02-007	Material Submittal for GRP Pipe	5	24-Dec-25	29-Dec-25	24-Dec-25A	29-Dec-25A	0.00	0.00	0.00	100%	100%	0
JDH4-02-007	Material Approval for GRP Pipe	5	24-Dec-25	29-Dec-25	24-Dec-25A	29-Dec-25A	28,182.47	28,182.47	28,182.47	100%	100%	0
Manholes		5	24-Dec-25	29-Dec-25	24-Dec-25A	29-Dec-25A	28,182.47	28,182.47	28,182.47	100%	100%	0
JDH4-02-007	Material Submittal for Manholes	5	24-Dec-25	29-Dec-25	24-Dec-25A	29-Dec-25A	0.00	0.00	0.00	100%	100%	0
JDH4-02-007	Material Approval for Manholes	5	24-Dec-25	29-Dec-25	24-Dec-25A	29-Dec-25A	28,182.47	28,182.47	28,182.47	100%	100%	0
TSE Network		15	24-Dec-25	10-Jan-26	24-Dec-25A	10-Jan-26A	84,547.41	84,547.41	84,547.41	100%	100%	0
HDPE Pipe (PN 16)		15	24-Dec-25	10-Jan-26	24-Dec-25A	10-Jan-26A	28,182.47	28,182.47	28,182.47	100%	100%	0

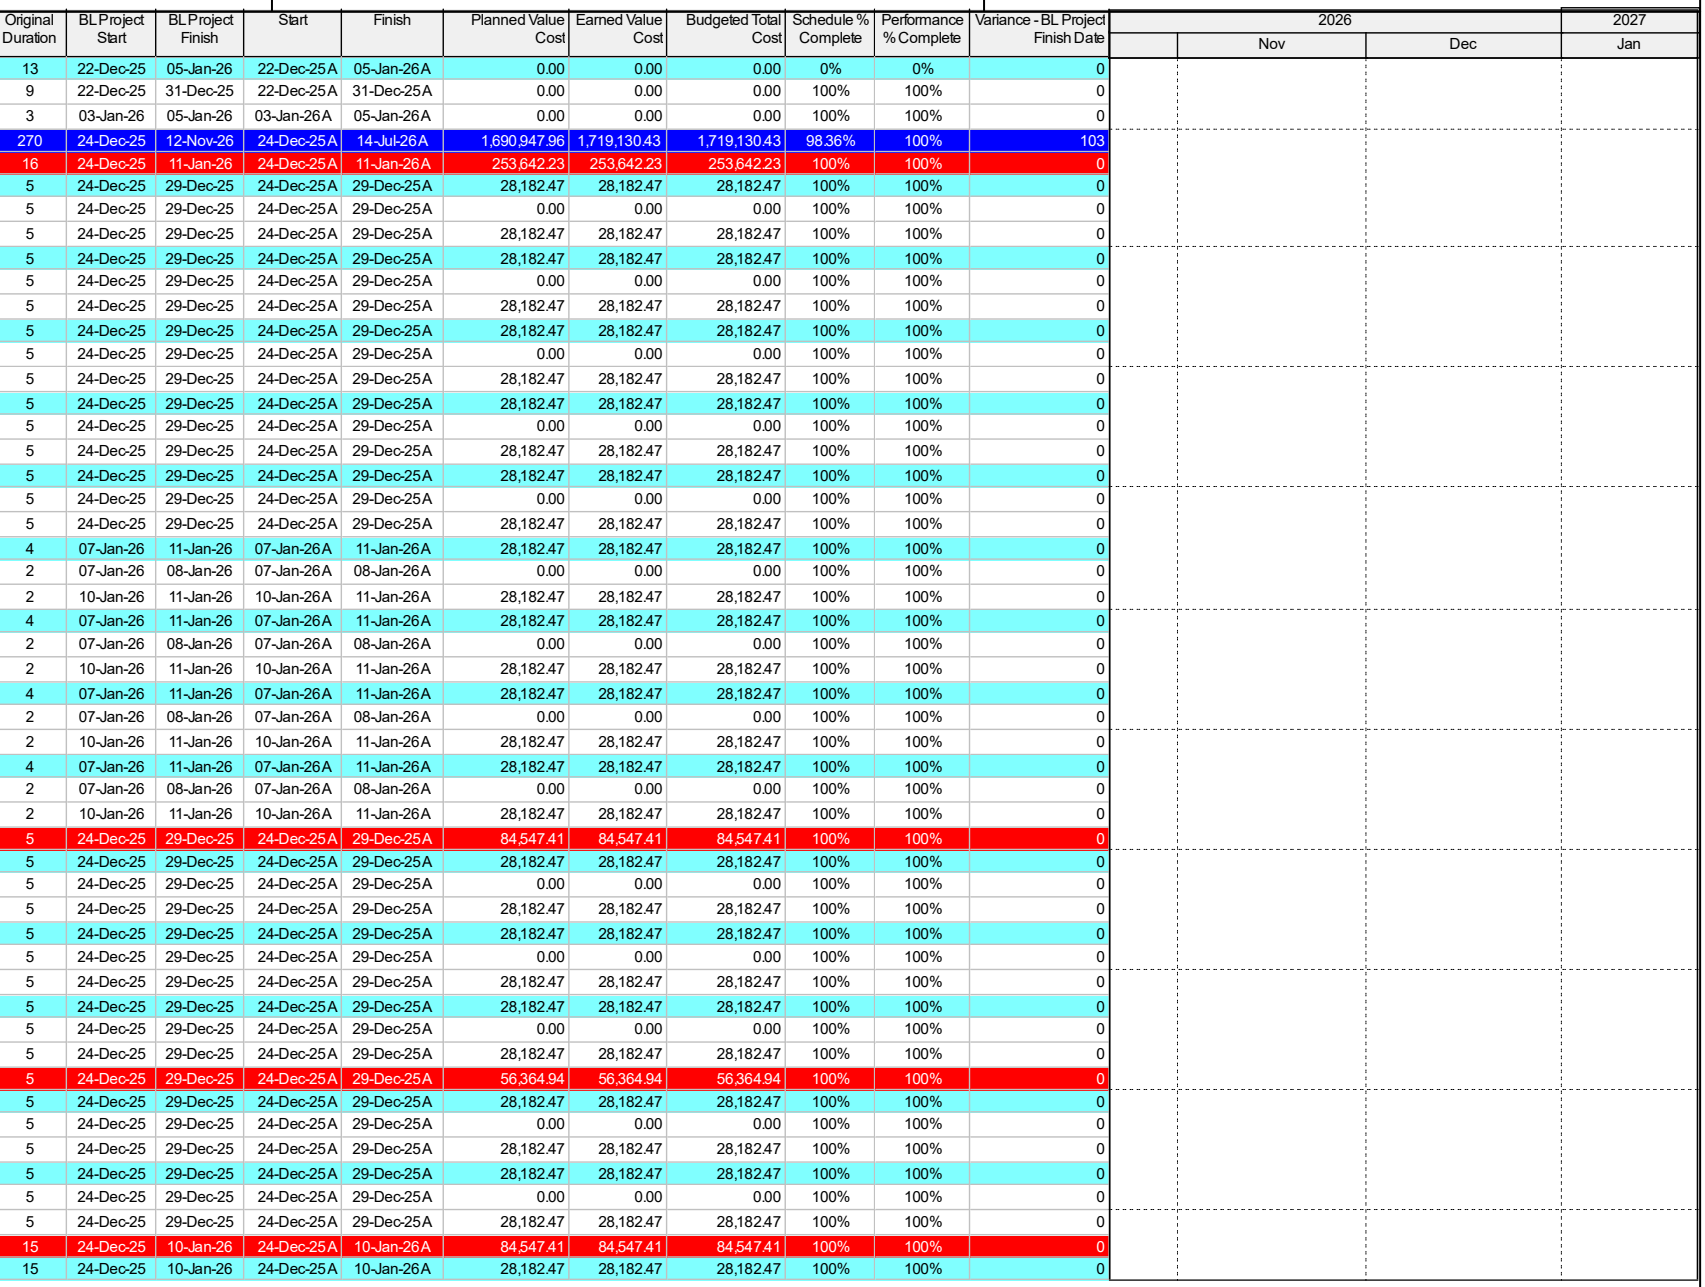


Date	Revision	Checked	Approved

Activity ID	Activity Name	Original Duration	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Schedule % Complete	Performance % Complete	Variance - BL Project Finish Date
JDH4-02-007	Material Submittal for HDPE Pipe (PI	5	24-Dec-25	29-Dec-25	24-Dec-25A	29-Dec-25A	0.00	0.00	0.00	100%	100%	0
JDH4-02-007	Material Approval for HDPE Pipe (PN	3	07-Jan-26	10-Jan-26	07-Jan-26A	10-Jan-26A	28,182.47	28,182.47	28,182.47	100%	100%	0
Valves / Chambers		3	07-Jan-26	10-Jan-26	07-Jan-26A	10-Jan-26A	28,182.47	28,182.47	28,182.47	100%	100%	0
JDH4-02-007	Material Submittal for Valves / Chamt	2	07-Jan-26	08-Jan-26	07-Jan-26A	08-Jan-26A	0.00	0.00	0.00	100%	100%	0
JDH4-02-007	Material Approval for Valves / Chamb	2	08-Jan-26	10-Jan-26	08-Jan-26A	10-Jan-26A	28,182.47	28,182.47	28,182.47	100%	100%	0
Risers		3	07-Jan-26	10-Jan-26	07-Jan-26A	10-Jan-26A	28,182.47	28,182.47	28,182.47	100%	100%	0
JDH4-02-007	Material Submittal for Risers	2	07-Jan-26	08-Jan-26	07-Jan-26A	08-Jan-26A	0.00	0.00	0.00	100%	100%	0
JDH4-02-007	Material Approval for Risers	2	08-Jan-26	10-Jan-26	08-Jan-26A	10-Jan-26A	28,182.47	28,182.47	28,182.47	100%	100%	0
Potable Water Network		15	24-Dec-25	10-Jan-26	24-Dec-25A	10-Jan-26A	84,547.41	84,547.41	84,547.41	100%	100%	0
HDPE Pipe (PN 16)		15	24-Dec-25	10-Jan-26	24-Dec-25A	10-Jan-26A	28,182.47	28,182.47	28,182.47	100%	100%	0
JDH4-02-007	Material Submittal for HDPE Pipe (PI	5	24-Dec-25	29-Dec-25	24-Dec-25A	29-Dec-25A	0.00	0.00	0.00	100%	100%	0
JDH4-02-007	Material Approval for HDPE Pipe (PN	3	07-Jan-26	10-Jan-26	07-Jan-26A	10-Jan-26A	28,182.47	28,182.47	28,182.47	100%	100%	0
Valves / Chambers		3	07-Jan-26	10-Jan-26	07-Jan-26A	10-Jan-26A	28,182.47	28,182.47	28,182.47	100%	100%	0
JDH4-02-007	Material Submittal for Valves / Chamt	3	07-Jan-26	10-Jan-26	07-Jan-26A	10-Jan-26A	0.00	0.00	0.00	100%	100%	0
JDH4-02-007	Material Approval for Valves / Chamb	2	08-Jan-26	10-Jan-26	08-Jan-26A	10-Jan-26A	28,182.47	28,182.47	28,182.47	100%	100%	0
Fire Hydrant		2	08-Jan-26	10-Jan-26	08-Jan-26A	10-Jan-26A	28,182.47	28,182.47	28,182.47	100%	100%	0
JDH4-02-007	Material Submittal for Fire Hydrant	2	08-Jan-26	10-Jan-26	08-Jan-26A	10-Jan-26A	0.00	0.00	0.00	100%	100%	0
JDH4-02-007	Material Approval for Fire Hydrant	1	10-Jan-26	10-Jan-26	10-Jan-26A	10-Jan-26A	28,182.47	28,182.47	28,182.47	100%	100%	0
Electrical Network		257	08-Jan-26	12-Nov-26	08-Jan-26A	11-Jun-26A	253,642.23	281,824.70	281,824.70	90%	100%	131
Pipe for the Duct		2	08-Jan-26	10-Jan-26	08-Jan-26A	10-Jan-26A	28,182.47	28,182.47	28,182.47	100%	100%	0
JDH4-02-007	Material Submittal for Pipe for the Duc	2	08-Jan-26	10-Jan-26	08-Jan-26A	10-Jan-26A	0.00	0.00	0.00	100%	100%	0
JDH4-02-007	Material Approval for Pipe for the Duc	1	10-Jan-26	10-Jan-26	10-Jan-26A	10-Jan-26A	28,182.47	28,182.47	28,182.47	100%	100%	0
Low Voltage Cables		5	10-Jan-26	14-Jan-26	10-Jan-26A	14-Jan-26A	28,182.47	28,182.47	28,182.47	100%	100%	0
JDH4-02-007	Material Submittal for Low Voltage Ca	1	10-Jan-26	10-Jan-26	10-Jan-26A	10-Jan-26A	0.00	0.00	0.00	100%	100%	0
JDH4-02-007	Material Approval for Low Voltage Ca	5	10-Jan-26	14-Jan-26	10-Jan-26A	14-Jan-26A	28,182.47	28,182.47	28,182.47	100%	100%	0
Earthing System		9	10-Jan-26	19-Jan-26	10-Jan-26A	19-Jan-26A	28,182.47	28,182.47	28,182.47	100%	100%	0
JDH4-02-007	Material Submittal for Earthing Syster	1	10-Jan-26	10-Jan-26	10-Jan-26A	10-Jan-26A	0.00	0.00	0.00	100%	100%	0
JDH4-02-007	Material Approval for Earthing Systen	3	17-Jan-26	19-Jan-26	17-Jan-26A	19-Jan-26A	28,182.47	28,182.47	28,182.47	100%	100%	0
Medium Voltage Cable		15	27-Oct-26	12-Nov-26	23-Mar-26A	03-Jun-26A	0.00	28,182.47	28,182.47	0%	100%	138
JDH4-02-007	Material Submittal for Medium Voltag	1	27-Oct-26	27-Oct-26	23-Mar-26A	31-Mar-26A	0.00	0.00	0.00	0%	100%	177
JDH4-02-007	Material Approval for Medium Voltag	14	28-Oct-26	12-Nov-26	01-Apr-26A	03-Jun-26A	0.00	28,182.47	28,182.47	0%	100%	138
Low Voltage Distribution Panel		9	10-Jan-26	19-Jan-26	10-Jan-26A	19-Jan-26A	28,182.47	28,182.47	28,182.47	100%	100%	0
JDH4-02-007	Material Submittal for Low Voltage Di	1	10-Jan-26	10-Jan-26	10-Jan-26A	10-Jan-26A	0.00	0.00	0.00	100%	100%	0
JDH4-02-007	Material Approval for Low Voltage Di	3	17-Jan-26	19-Jan-26	17-Jan-26A	19-Jan-26A	28,182.47	28,182.47	28,182.47	100%	100%	0
Unit Sub Station		141	11-Jan-26	24-Feb-26	11-Jan-26A	06-Jun-26A	28,182.47	28,182.47	28,182.47	100%	100%	-81
JDH4-02-007	Material Submittal for Unit Sub Statio	1	11-Jan-26	11-Jan-26	11-Jan-26A	23-Apr-26A	0.00	0.00	0.00	100%	100%	-84
JDH4-02-007	Material Approval for Unit Sub Statior	7	16-Feb-26	24-Feb-26	25-Apr-26A	06-Jun-26A	28,182.47	28,182.47	28,182.47	100%	100%	-81
Ring Main Unit (RMU)		135	11-Jan-26	26-Feb-26	11-Jan-26A	03-Jun-26A	28,182.47	28,182.47	28,182.47	100%	100%	-77
JDH4-02-007	Material Submittal for Ring main Unit	1	11-Jan-26	11-Jan-26	11-Jan-26A	23-Apr-26A	0.00	0.00	0.00	100%	100%	-84
JDH4-02-007	Material Approval for Ring main Unit	7	18-Feb-26	26-Feb-26	25-Apr-26A	03-Jun-26A	28,182.47	28,182.47	28,182.47	100%	100%	-77
Lighting poles		9	10-Jan-26	19-Jan-26	10-Jan-26A	19-Jan-26A	28,182.47	28,182.47	28,182.47	100%	100%	0
JDH4-02-007	Material Submittal for Lighting poles	1	10-Jan-26	10-Jan-26	10-Jan-26A	10-Jan-26A	0.00	0.00	0.00	100%	100%	0
JDH4-02-007	Material Approval for Lighting poles E	3	17-Jan-26	19-Jan-26	17-Jan-26A	19-Jan-26A	28,182.47	28,182.47	28,182.47	100%	100%	0
Lighting panels/Feeder Pillers		130	17-Jan-26	07-Mar-26	17-Jan-26A	11-Jun-26A	28,182.47	28,182.47	28,182.47	100%	100%	-77
JDH4-02-007	Material Submittal for Lighting panels	3	17-Jan-26	19-Jan-26	17-Jan-26A	19-Jan-26A	0.00	0.00	0.00	100%	100%	0
JDH4-02-007	Material Approval for Lighting panels,	7	28-Feb-26	07-Mar-26	20-Jan-26A	11-Jun-26A	28,182.47	28,182.47	28,182.47	100%	100%	-77
Street Lighting Luminaire		9	10-Jan-26	19-Jan-26	10-Jan-26A	19-Jan-26A	28,182.47	28,182.47	28,182.47	100%	100%	0
JDH4-02-007	Material Submittal for Street Lighting I	1	10-Jan-26	10-Jan-26	10-Jan-26A	10-Jan-26A	0.00	0.00	0.00	100%	100%	0
JDH4-02-007	Material Approval for Street Lighting L	3	17-Jan-26	19-Jan-26	17-Jan-26A	19-Jan-26A	28,182.47	28,182.47	28,182.47	100%	100%	0
Telecommunications		3	27-Dec-25	29-Dec-25	26-Dec-25A	29-Dec-25A	28,182.47	28,182.47	28,182.47	100%	100%	0
Pipe for the Duct		3	27-Dec-25	29-Dec-25	26-Dec-25A	29-Dec-25A	28,182.47	28,182.47	28,182.47	100%	100%	0

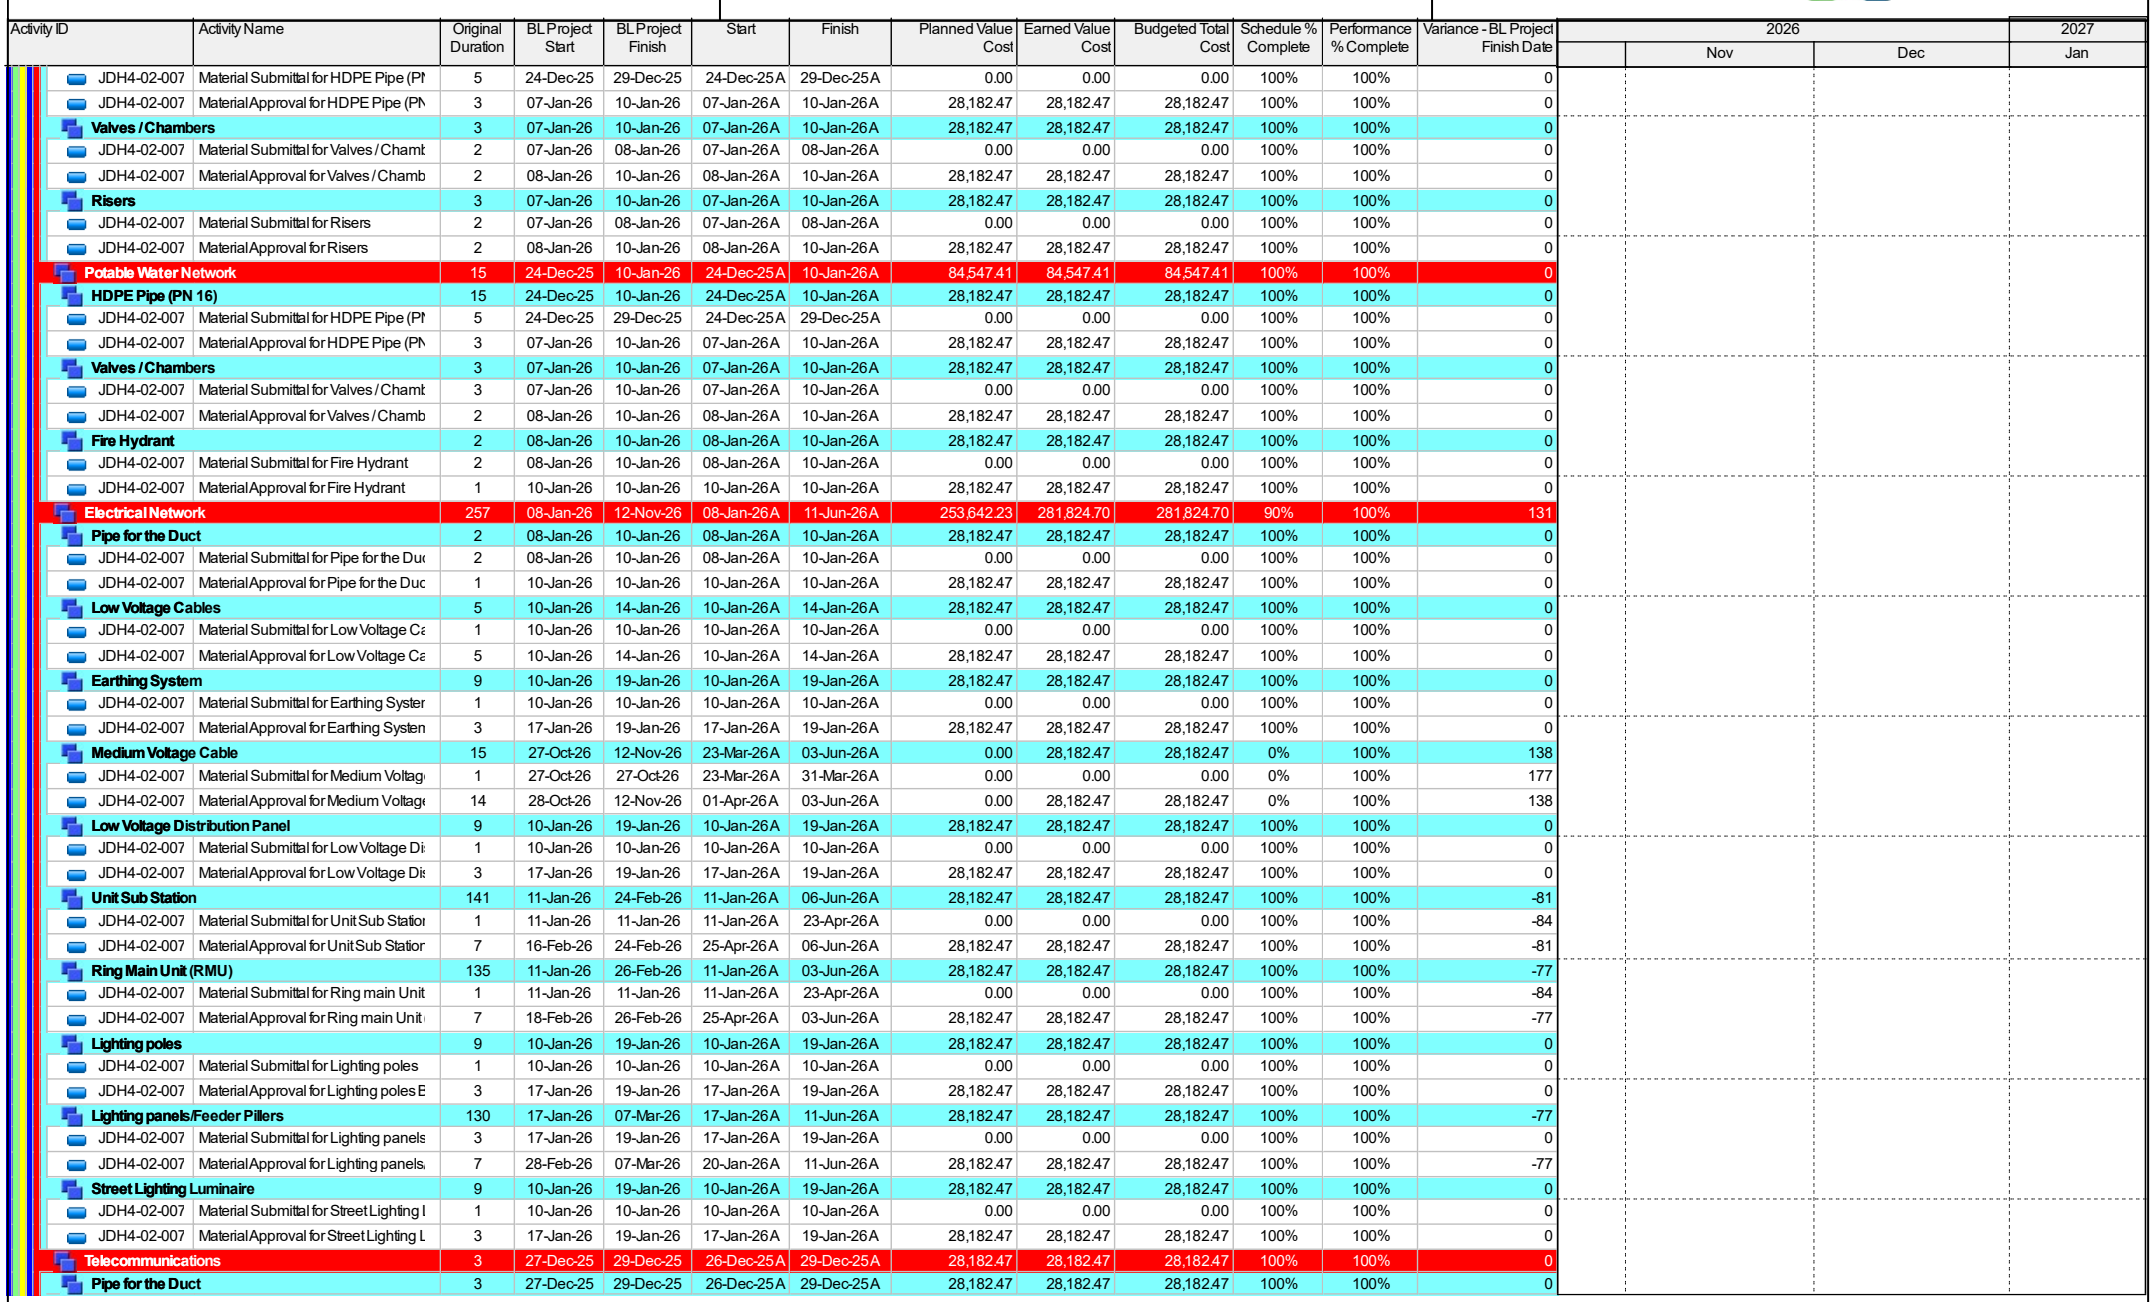


Date	Revision	Checked	Approved

Activity ID	Activity Name	Original Duration	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Schedule % Complete	Performance % Complete	Variance - BL Project Finish Date
JDH4-02-007	Material Submittal for Pipe for the Duc	3	27-Dec-25	29-Dec-25	26-Dec-25 A	29-Dec-25 A	0.00	0.00	0.00	100%	100%	0
JDH4-02-007	Material Approval for Pipe for the Duc	3	27-Dec-25	29-Dec-25	26-Dec-25 A	29-Dec-25 A	28,182.47	28,182.47	28,182.47	100%	100%	0
Sewage Lift Station		185	01-Jan-26	29-Mar-26	01-Jan-26 A	14-Jul-26 A	845,473.86	845,473.86	845,473.86	100%	100%	-89
Thermal & Moisture Protection		12	25-Feb-26	10-Mar-26	01-Jan-26 A	04-Jan-26 A	28,182.47	28,182.47	28,182.47	100%	100%	55
JDH4-02-007	Material Submittal for Thermal & Mois	5	25-Feb-26	02-Mar-26	01-Jan-26 A	01-Jan-26 A	0.00	0.00	0.00	100%	100%	50
JDH4-02-007	Material Approval for Thermal & Mois	7	03-Mar-26	10-Mar-26	03-Jan-26 A	04-Jan-26 A	28,182.47	28,182.47	28,182.47	100%	100%	55
Metals		12	25-Feb-26	10-Mar-26	19-Feb-26 A	25-Feb-26 A	28,182.47	28,182.47	28,182.47	100%	100%	11
JDH4-02-007	Material Submittal for Metal	5	25-Feb-26	02-Mar-26	19-Feb-26 A	19-Feb-26 A	0.00	0.00	0.00	100%	100%	8
JDH4-02-007	Material Approval for Metal	7	03-Mar-26	10-Mar-26	21-Feb-26 A	25-Feb-26 A	28,182.47	28,182.47	28,182.47	100%	100%	11
Pumps		9	10-Jan-26	19-Jan-26	10-Jan-26 A	19-Jan-26 A	28,182.47	28,182.47	28,182.47	100%	100%	0
JDH4-02-007	Material Submittal for pumps	1	10-Jan-26	10-Jan-26	10-Jan-26 A	10-Jan-26 A	0.00	0.00	0.00	100%	100%	0
JDH4-02-007	Material Approval for pumps	3	17-Jan-26	19-Jan-26	17-Jan-26 A	19-Jan-26 A	28,182.47	28,182.47	28,182.47	100%	100%	0
Pipes,Fittings & Valves		5	10-Jan-26	14-Jan-26	10-Jan-26 A	14-Jan-26 A	28,182.47	28,182.47	28,182.47	100%	100%	0
JDH4-02-007	Material Submittal for Pipes,Fittings &	1	10-Jan-26	10-Jan-26	10-Jan-26 A	10-Jan-26 A	0.00	0.00	0.00	100%	100%	0
JDH4-02-007	Material Approval for Pipes,Fittings &	5	10-Jan-26	14-Jan-26	10-Jan-26 A	14-Jan-26 A	28,182.47	28,182.47	28,182.47	100%	100%	0
Odours scrubbing system		5	22-Jan-26	27-Jan-26	22-Jan-26 A	27-Jan-26 A	28,182.47	28,182.47	28,182.47	100%	100%	0
JDH4-02-007	Material Submittal for Odours Scrubb	1	22-Jan-26	22-Jan-26	22-Jan-26 A	22-Jan-26 A	0.00	0.00	0.00	100%	100%	0
JDH4-02-007	Material Approval for Odours Scrubb	5	22-Jan-26	27-Jan-26	22-Jan-26 A	27-Jan-26 A	28,182.47	28,182.47	28,182.47	100%	100%	0
Crane		4	17-Jan-26	20-Jan-26	17-Jan-26 A	20-Jan-26 A	28,182.47	28,182.47	28,182.47	100%	100%	0
JDH4-02-007	Material Submittal for Crane	2	17-Jan-26	18-Jan-26	17-Jan-26 A	18-Jan-26 A	0.00	0.00	0.00	100%	100%	0
JDH4-02-007	Material Approval for Crane	4	17-Jan-26	20-Jan-26	17-Jan-26 A	20-Jan-26 A	28,182.47	28,182.47	28,182.47	100%	100%	0
Air Vents		3	21-Jan-26	24-Jan-26	21-Jan-26 A	24-Jan-26 A	28,182.47	28,182.47	28,182.47	100%	100%	0
JDH4-02-007	Material Submittal for Air Vents	2	21-Jan-26	22-Jan-26	21-Jan-26 A	22-Jan-26 A	0.00	0.00	0.00	100%	100%	0
JDH4-02-007	Material Approval for Air Vents	2	22-Jan-26	24-Jan-26	22-Jan-26 A	24-Jan-26 A	28,182.47	28,182.47	28,182.47	100%	100%	0
Screening Container		12	07-Mar-26	23-Mar-26	08-Feb-26 A	01-Mar-26 A	28,182.47	28,182.47	28,182.47	100%	100%	16
JDH4-02-007	Material Submittal for Screening Con	5	07-Mar-26	11-Mar-26	08-Feb-26 A	08-Feb-26 A	0.00	0.00	0.00	100%	100%	26
JDH4-02-007	Material Approval for Screening Con	7	12-Mar-26	23-Mar-26	10-Feb-26 A	01-Mar-26 A	28,182.47	28,182.47	28,182.47	100%	100%	16
Baffle Plates		5	14-Jan-26	19-Jan-26	14-Jan-26 A	19-Jan-26 A	28,182.47	28,182.47	28,182.47	100%	100%	0
JDH4-02-007	Material Submittal for Baffle plates	1	14-Jan-26	14-Jan-26	14-Jan-26 A	14-Jan-26 A	0.00	0.00	0.00	100%	100%	0
JDH4-02-007	Material Approval for Baffle plates	4	15-Jan-26	19-Jan-26	15-Jan-26 A	19-Jan-26 A	28,182.47	28,182.47	28,182.47	100%	100%	0
Anti-Water Hammer Equipment		12	12-Mar-26	29-Mar-26	08-Feb-26 A	09-Feb-26 A	28,182.47	28,182.47	28,182.47	100%	100%	37
JDH4-02-007	Material Submittal for Anti-Water Han	5	12-Mar-26	17-Mar-26	08-Feb-26 A	08-Feb-26 A	0.00	0.00	0.00	100%	100%	31
JDH4-02-007	Material Approval for Anti-Water Han	7	22-Mar-26	29-Mar-26	09-Feb-26 A	09-Feb-26 A	28,182.47	28,182.47	28,182.47	100%	100%	37
Air Conditioning and Ventilation		4	14-Jan-26	18-Jan-26	14-Jan-26 A	18-Jan-26 A	28,182.47	28,182.47	28,182.47	100%	100%	0
JDH4-02-007	Material Submittal for Air Conditioning	1	14-Jan-26	14-Jan-26	14-Jan-26 A	14-Jan-26 A	0.00	0.00	0.00	100%	100%	0
JDH4-02-007	Material Approval for Air Conditioning	3	15-Jan-26	18-Jan-26	15-Jan-26 A	18-Jan-26 A	28,182.47	28,182.47	28,182.47	100%	100%	0
Fuel System		42	17-Jan-26	07-Mar-26	17-Jan-26 A	10-Feb-26 A	28,182.23	28,182.23	28,182.23	100%	100%	20
JDH4-02-007	Material Submittal for Fuel System	3	17-Jan-26	19-Jan-26	17-Jan-26 A	19-Jan-26 A	0.00	0.00	0.00	100%	100%	0
JDH4-02-007	Material Approval for Fuel System(Cc	3	29-Jan-26	01-Feb-26	29-Jan-26 A	01-Feb-26 A	14,091.23	14,091.23	14,091.23	100%	100%	0
JDH4-02-007	Material Approval for Fuel System	7	28-Feb-26	07-Mar-26	09-Feb-26 A	10-Feb-26 A	14,091.00	14,091.00	14,091.00	100%	100%	20
Fire Fighting System		46	17-Jan-26	10-Mar-26	16-Jan-26 A	19-Feb-26 A	28,182.47	28,182.47	28,182.47	100%	100%	15
JDH4-02-007	Material Submittal for Fire Fighting Sy	3	17-Jan-26	19-Jan-26	16-Jan-26 A	17-Feb-26 A	0.00	0.00	0.00	100%	100%	-25
JDH4-02-007	Material Approval for Fire Fighting Sy	7	03-Mar-26	10-Mar-26	17-Feb-26 A	19-Feb-26 A	28,182.47	28,182.47	28,182.47	100%	100%	15
Main Distribution Board /MCC panels		130	17-Jan-26	04-Mar-26	17-Jan-26 A	07-Jun-26 A	28,182.47	28,182.47	28,182.47	100%	100%	-75
JDH4-02-007	Material Submittal for Main Distributio	3	17-Jan-26	19-Jan-26	17-Jan-26 A	19-Jan-26 A	0.00	0.00	0.00	100%	100%	0
JDH4-02-007	Material Approval for Main Distributio	7	25-Feb-26	04-Mar-26	20-Jan-26 A	07-Jun-26 A	28,182.47	28,182.47	28,182.47	100%	100%	-75
Final Panel boards		133	13-Jan-26	28-Feb-26	13-Jan-26 A	07-Jun-26 A	28,182.47	28,182.47	28,182.47	100%	100%	-79
JDH4-02-007	Material Submittal for Final Panel Boa	2	13-Jan-26	14-Jan-26	13-Jan-26 A	14-Jan-26 A	0.00	0.00	0.00	100%	100%	0
JDH4-02-007	Material Approval for Final Panel Boa	7	19-Feb-26	28-Feb-26	15-Jan-26 A	07-Jun-26 A	28,182.47	28,182.47	28,182.47	100%	100%	-79
Local Control Panel/ Monitoring Control Panel		68	13-Jan-26	08-Mar-26	13-Jan-26 A	02-Feb-26 A	28,182.47	28,182.47	28,182.47	100%	100%	28
JDH4-02-007	Material Submittal for Local Control P	2	13-Jan-26	14-Jan-26	13-Jan-26 A	14-Jan-26 A	0.00	0.00	0.00	100%	100%	0

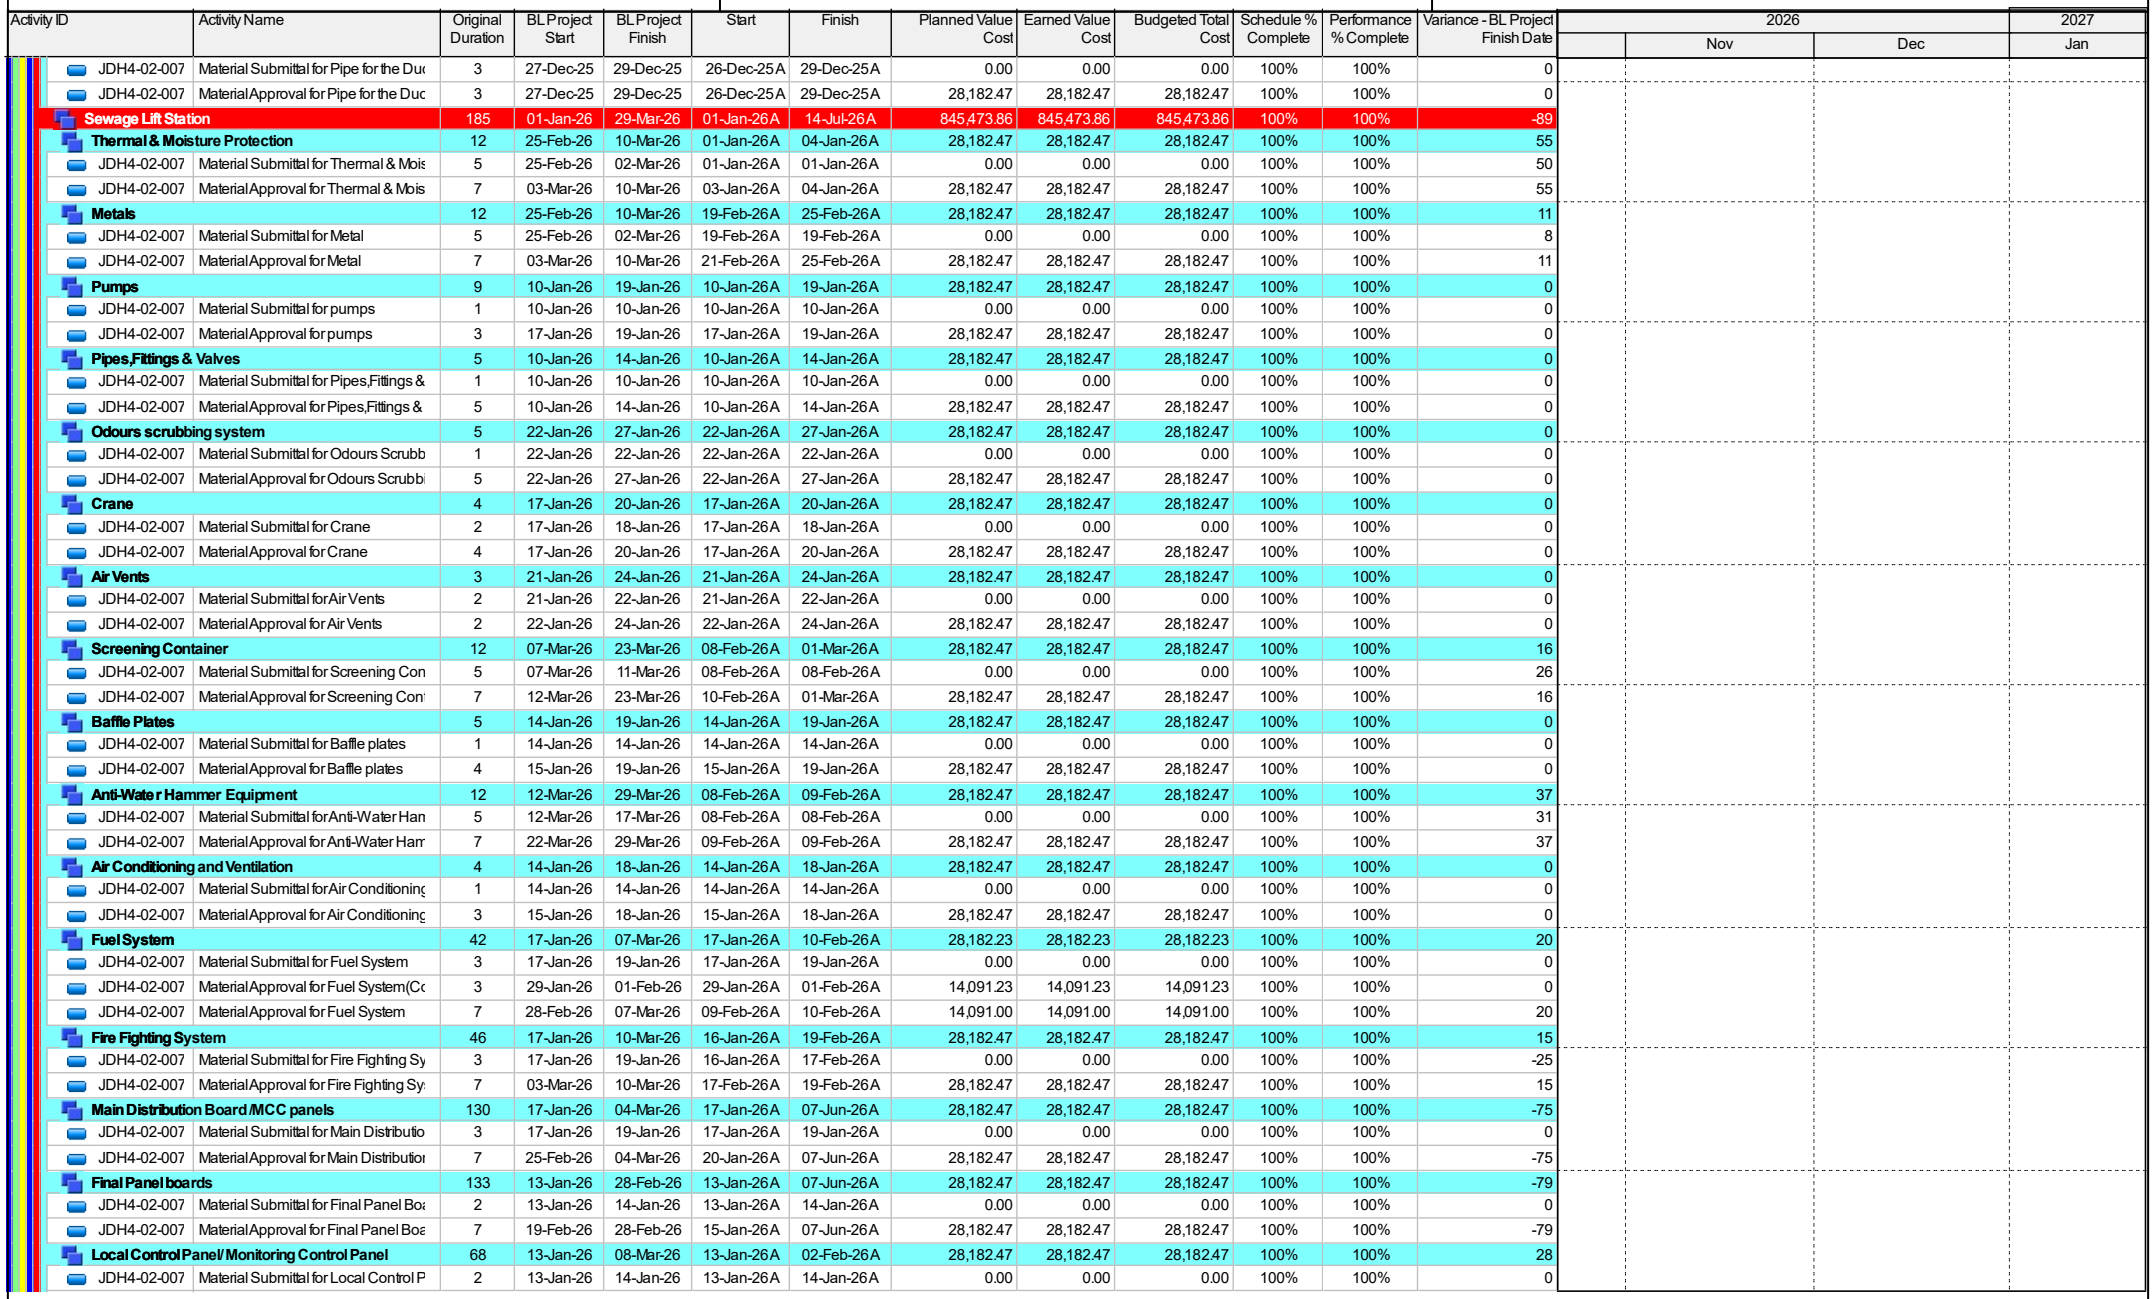


Date	Revision	Checked	Approved

Activity ID	Activity Name	Original Duration	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Schedule % Complete	Performance % Complete	Variance - BL Project Finish Date
JDH4-02-007	Material Approval for Local Control P	7	01-Mar-26	08-Mar-26	14-Jan-26 A	02-Feb-26 A	28,182.47	28,182.47	28,182.47	100%	100%	28
Engine Generators		7	12-Jan-26	19-Jan-26	12-Jan-26 A	19-Jan-26 A	28,182.47	28,182.47	28,182.47	100%	100%	0
JDH4-02-007	Material Submittal for Engine Genera	2	12-Jan-26	13-Jan-26	12-Jan-26 A	13-Jan-26 A	0.00	0.00	0.00	100%	100%	0
JDH4-02-007	Material Approval for Engine Genera	3	17-Jan-26	19-Jan-26	17-Jan-26 A	19-Jan-26 A	28,182.47	28,182.47	28,182.47	100%	100%	0
Standby Diesel Generator		6	13-Jan-26	19-Jan-26	13-Jan-26 A	19-Jan-26 A	28,182.47	28,182.47	28,182.47	100%	100%	0
JDH4-02-007	Material Submittal for Standby Diesel	2	13-Jan-26	14-Jan-26	13-Jan-26 A	14-Jan-26 A	0.00	0.00	0.00	100%	100%	0
JDH4-02-007	Material Approval for Standby Diesel	3	17-Jan-26	19-Jan-26	17-Jan-26 A	19-Jan-26 A	28,182.47	28,182.47	28,182.47	100%	100%	0
Power Factor Correction Capacitor Bank		172	17-Jan-26	28-Feb-26	17-Jan-26 A	14-Jul-26 A	28,182.47	28,182.47	28,182.47	100%	100%	-111
JDH4-02-007	Material Submittal for Power Factor c	3	17-Jan-26	19-Jan-26	17-Jan-26 A	19-Jan-26 A	0.00	0.00	0.00	100%	100%	0
JDH4-02-007	Material Approval for Power Factor cc	7	19-Feb-26	28-Feb-26	12-Jul-26 A	14-Jul-26 A	28,182.47	28,182.47	28,182.47	100%	100%	-111
Low-Voltage Electrical Power Conductors and Cab		9	10-Jan-26	19-Jan-26	10-Jan-26 A	19-Jan-26 A	28,182.47	28,182.47	28,182.47	100%	100%	0
JDH4-02-007	Material Submittal for Low Voltage Ele	1	10-Jan-26	10-Jan-26	10-Jan-26 A	10-Jan-26 A	0.00	0.00	0.00	100%	100%	0
JDH4-02-007	Material Approval for Low Voltage Ele	3	17-Jan-26	19-Jan-26	17-Jan-26 A	19-Jan-26 A	28,182.47	28,182.47	28,182.47	100%	100%	0
Low Voltage Feeder Cable		9	10-Jan-26	19-Jan-26	10-Jan-26 A	19-Jan-26 A	28,182.47	28,182.47	28,182.47	100%	100%	0
JDH4-02-007	Material Submittal for Low Voltage Fe	1	10-Jan-26	10-Jan-26	10-Jan-26 A	10-Jan-26 A	0.00	0.00	0.00	100%	100%	0
JDH4-02-007	Material Approval for Low Voltage Fe	3	17-Jan-26	19-Jan-26	17-Jan-26 A	19-Jan-26 A	28,182.47	28,182.47	28,182.47	100%	100%	0
Wiring Devices		43	10-Jan-26	01-Mar-26	10-Jan-26 A	28-Jan-26 A	28,182.47	28,182.47	28,182.47	100%	100%	26
JDH4-02-007	Material Submittal for Wiring Devices	1	10-Jan-26	10-Jan-26	10-Jan-26 A	10-Jan-26 A	0.00	0.00	0.00	100%	100%	0
JDH4-02-007	Material Approval for Wiring Devices	7	21-Feb-26	01-Mar-26	11-Jan-26 A	28-Jan-26 A	28,182.47	28,182.47	28,182.47	100%	100%	26
Enclosed Switches and Circuit Breakers		9	10-Jan-26	19-Jan-26	10-Jan-26 A	19-Jan-26 A	28,182.47	28,182.47	28,182.47	100%	100%	0
JDH4-02-007	Material Submittal for Enclosed Switc	1	10-Jan-26	10-Jan-26	10-Jan-26 A	10-Jan-26 A	0.00	0.00	0.00	100%	100%	0
JDH4-02-007	Material Approval for Enclosed Switcl	3	17-Jan-26	19-Jan-26	17-Jan-26 A	19-Jan-26 A	28,182.47	28,182.47	28,182.47	100%	100%	0
Raceways for Electrical Systems		12	16-Feb-26	02-Mar-26	13-Jan-26 A	20-Jan-26 A	28,182.47	28,182.47	28,182.47	100%	100%	34
JDH4-02-007	Material Submittal for Raceways for E	5	16-Feb-26	21-Feb-26	13-Jan-26 A	14-Jan-26 A	0.00	0.00	0.00	100%	100%	32
JDH4-02-007	Material Approval for Raceways for E	7	23-Feb-26	02-Mar-26	15-Jan-26 A	20-Jan-26 A	28,182.47	28,182.47	28,182.47	100%	100%	34
Electrical Manholes		6	01-Jan-26	07-Jan-26	01-Jan-26 A	07-Jan-26 A	28,182.47	28,182.47	28,182.47	100%	100%	0
JDH4-02-007	Material Submittal for Electrical Manh	2	01-Jan-26	03-Jan-26	01-Jan-26 A	03-Jan-26 A	0.00	0.00	0.00	100%	100%	0
JDH4-02-007	Material Approval for Electrical Manhc	4	04-Jan-26	07-Jan-26	04-Jan-26 A	07-Jan-26 A	28,182.47	28,182.47	28,182.47	100%	100%	0
Security System (CCTV System)		6	13-Jan-26	19-Jan-26	13-Jan-26 A	19-Jan-26 A	28,182.47	28,182.47	28,182.47	100%	100%	0
JDH4-02-007	Material Submittal for Security Systen	2	13-Jan-26	14-Jan-26	13-Jan-26 A	14-Jan-26 A	0.00	0.00	0.00	100%	100%	0
JDH4-02-007	Material Approval for Security System	3	17-Jan-26	19-Jan-26	17-Jan-26 A	19-Jan-26 A	28,182.47	28,182.47	28,182.47	100%	100%	0
ICT (Data& telephone System)		6	13-Jan-26	19-Jan-26	13-Jan-26 A	19-Jan-26 A	28,182.47	28,182.47	28,182.47	100%	100%	0
JDH4-02-007	Material Submittal for ICT (Data & Tel	2	13-Jan-26	14-Jan-26	13-Jan-26 A	14-Jan-26 A	0.00	0.00	0.00	100%	100%	0
JDH4-02-007	Material Approval for ICT (Data & Tel	3	17-Jan-26	19-Jan-26	17-Jan-26 A	19-Jan-26 A	28,182.47	28,182.47	28,182.47	100%	100%	0
Programmable Logic Controllers		12	23-Feb-26	08-Mar-26	01-Feb-26 A	02-Feb-26 A	28,182.47	28,182.47	28,182.47	100%	100%	28
JDH4-02-007	Material Submittal for Programmable	5	23-Feb-26	28-Feb-26	01-Feb-26 A	01-Feb-26 A	0.00	0.00	0.00	100%	100%	22
JDH4-02-007	Material Approval for Programmable	7	01-Mar-26	08-Mar-26	02-Feb-26 A	02-Feb-26 A	28,182.47	28,182.47	28,182.47	100%	100%	28
Process Control Wiring		34	17-Jan-26	25-Feb-26	17-Jan-26 A	08-Feb-26 A	28,182.47	28,182.47	28,182.47	100%	100%	14
JDH4-02-007	Material Submittal for Process Contro	2	17-Jan-26	18-Jan-26	17-Jan-26 A	18-Jan-26 A	0.00	0.00	0.00	100%	100%	0
JDH4-02-007	Material Approval for Process Contro	7	17-Feb-26	25-Feb-26	02-Feb-26 A	08-Feb-26 A	28,182.47	28,182.47	28,182.47	100%	100%	14
Instrumentation for Process Systems		9	17-Jan-26	26-Jan-26	17-Jan-26 A	26-Jan-26 A	28,182.47	28,182.47	28,182.47	100%	100%	0
JDH4-02-007	Material Submittal for Instrumentation	2	17-Jan-26	18-Jan-26	17-Jan-26 A	18-Jan-26 A	0.00	0.00	0.00	100%	100%	0
JDH4-02-007	Material Approval for Instrumentation	5	21-Jan-26	26-Jan-26	21-Jan-26 A	26-Jan-26 A	28,182.47	28,182.47	28,182.47	100%	100%	0
Procurement		369	27-Dec-25	31-Dec-26	27-Dec-25 A	06-Oct-26 A	10,181,328.28	11,460,869.58	11,460,869.58	88.84%	100%	74
Short Lead Item		291	27-Dec-25	01-Sep-26	27-Dec-25 A	29-Sep-26 A	5,193,206.43	5,193,206.43	5,193,206.43	100%	100%	-23
Road Works - Civil		205	31-Dec-25	08-Aug-26	31-Dec-25 A	29-Sep-26 A	1,611,684.79	1,611,684.79	1,611,684.79	100%	100%	-44
Steel Reinforcement		69	31-Dec-25	25-Mar-26	31-Dec-25 A	02-Feb-26 A	179,076.06	179,076.06	179,076.06	100%	100%	40
JDH4-02-007-	PO for Steel Reinforcement	3	31-Dec-25	03-Jan-26	31-Dec-25 A	03-Jan-26 A	0.00	0.00	0.00	100%	100%	0
JDH4-02-007-	Material Fabrication for Steel Reinfor	1	03-Jan-26	03-Jan-26	03-Jan-26 A	03-Jan-26 A	0.00	0.00	0.00	100%	100%	0
JDH4-02-007-	Material Delivery for Steel Reinforcer	4	28-Jan-26	01-Feb-26	28-Jan-26 A	01-Feb-26 A	35,815.22	35,815.22	35,815.22	100%	100%	0
JDH4-02-007-	Material Delivery for Steel Reinforcer	11	15-Feb-26	28-Feb-26	28-Jan-26 A	29-Jan-26 A	53,722.79	53,722.79	53,722.79	100%	100%	24

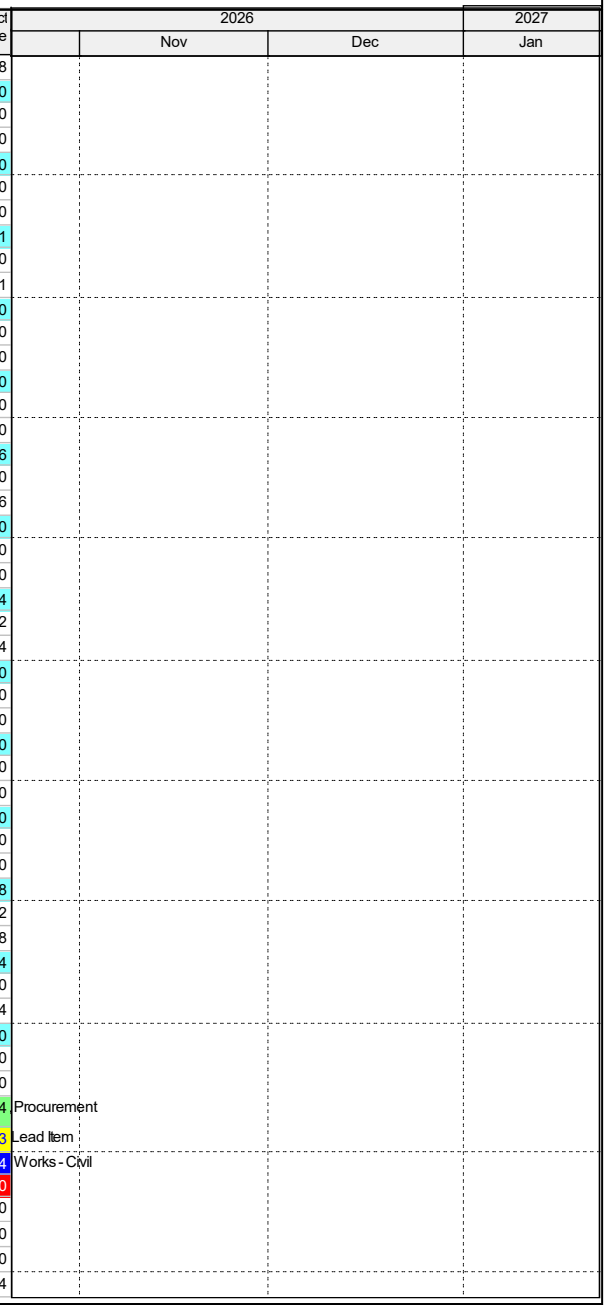


Date	Revision	Checked	Approved

Activity ID	Activity Name	Original Duration	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Schedule % Complete	Performance % Complete	Variance - BL Project Finish Date
JDH4-02-007-	Material Delivery for Steel Reinforcer	19	01-Mar-26	25-Mar-26	31-Jan-26 A	02-Feb-26 A	89,538.05	89,538.05	89,538.05	100%	100%	40
Ready Mixed Concrete		5	31-Dec-25	05-Jan-26	31-Dec-25 A	05-Jan-26 A	179,076.09	179,076.09	179,076.09	100%	100%	0
JDH4-02-007-	PO for Ready Mixed Concrete	3	31-Dec-25	03-Jan-26	31-Dec-25 A	03-Jan-26 A	0.00	0.00	0.00	100%	100%	0
JDH4-02-007-	Material Delivery for Ready Mixed Cc	3	03-Jan-26	05-Jan-26	03-Jan-26 A	05-Jan-26 A	179,076.09	179,076.09	179,076.09	100%	100%	0
Water Proofing		55	17-Feb-26	26-Apr-26	01-Jan-26 A	19-Feb-26 A	179,076.09	179,076.09	179,076.09	100%	100%	52
JDH4-02-007-	PO for Water Proofing	5	17-Feb-26	23-Feb-26	01-Jan-26 A	05-Jan-26 A	0.00	0.00	0.00	100%	100%	41
JDH4-02-007-	Material Fabrication for Water Proofir	25	24-Feb-26	28-Mar-26	06-Jan-26 A	15-Jan-26 A	0.00	0.00	0.00	100%	100%	57
JDH4-02-007-	Material Delivery for Water Proofing	25	29-Mar-26	26-Apr-26	17-Jan-26 A	19-Feb-26 A	179,076.09	179,076.09	179,076.09	100%	100%	52
Aggregate Base Course		78	21-Feb-26	02-Jul-26	08-Apr-26 A	03-Aug-26 A	179,076.10	179,076.10	179,076.10	100%	100%	-27
JDH4-02-007-	PO for Aggregate Base Course	5	21-Feb-26	26-Feb-26	08-Apr-26 A	11-Apr-26 A	0.00	0.00	0.00	100%	100%	-34
JDH4-02-007-	Material Delivery for Aggregate Base	20	14-May-26	09-Jun-26	06-May-26 A	04-Jul-26 A	89,538.05	89,538.05	89,538.05	100%	100%	-21
JDH4-02-007-	Material Delivery for Aggregate Base	20	10-Jun-26	02-Jul-26	23-Jul-26 A	03-Aug-26 A	89,538.05	89,538.05	89,538.05	100%	100%	-27
Bituminous Base & Wearing Course		43	28-Feb-26	06-Jul-26	04-Mar-26 A	29-Sep-26 A	179,076.09	179,076.09	179,076.09	100%	100%	-72
JDH4-02-007-	PO for Bituminous Base & Wearing (	5	28-Feb-26	04-Mar-26	04-Mar-26 A	08-Apr-26 A	0.00	0.00	0.00	100%	100%	-27
JDH4-02-007-	Material Delivery to the Site	30	02-Jun-26	06-Jul-26	16-Apr-26 A	29-Sep-26 A	179,076.09	179,076.09	179,076.09	100%	100%	-72
Precast Concrete Kerb		63	05-Mar-26	08-Aug-26	11-Mar-26 A	30-Jul-26 A	179,076.09	179,076.09	179,076.09	100%	100%	7
JDH4-02-007-	PO for Precast Concrete Kerb	5	05-Mar-26	10-Mar-26	11-Mar-26 A	11-Mar-26 A	0.00	0.00	0.00	100%	100%	-1
JDH4-02-007-	Material Fabrication for Precast Conc	30	11-Mar-26	18-Apr-26	12-Mar-26 A	23-Apr-26 A	0.00	0.00	0.00	100%	100%	-5
JDH4-02-007-	Material Delivery for Precast Concret	28	07-Jul-26	08-Aug-26	25-Apr-26 A	30-Jul-26 A	179,076.09	179,076.09	179,076.09	100%	100%	7
Interlocking Block Pavers		61	11-Mar-26	24-May-26	01-Jun-26 A	30-Jul-26 A	179,076.09	179,076.09	179,076.09	100%	100%	-54
JDH4-02-007-	PO for Interlocking Block Pavers	3	11-Mar-26	14-Mar-26	01-Jun-26 A	03-Jun-26 A	0.00	0.00	0.00	100%	100%	-64
JDH4-02-007-	Material Fabrication for Interlocking B	30	15-Mar-26	21-Apr-26	04-Jun-26 A	21-Jun-26 A	0.00	0.00	0.00	100%	100%	-49
JDH4-02-007-	Material Delivery for Interlocking Bloc	28	22-Apr-26	24-May-26	13-Jun-26 A	30-Jul-26 A	179,076.09	179,076.09	179,076.09	100%	100%	-54
Pavement Markings		62	15-Mar-26	01-Jun-26	07-May-26 A	21-Jun-26 A	179,076.09	179,076.09	179,076.09	100%	100%	-17
JDH4-02-007-	PO for Pavement Markings	4	15-Mar-26	22-Mar-26	07-May-26 A	15-Jun-26 A	0.00	0.00	0.00	100%	100%	-70
JDH4-02-007-	Material Fabrication for Pavement Ma	30	23-Mar-26	26-Apr-26	16-Jun-26 A	21-Jun-26 A	0.00	0.00	0.00	100%	100%	-45
JDH4-02-007-	Material Delivery for Pavement Marki	28	27-Apr-26	01-Jun-26	24-May-26 A	13-Jun-26 A	179,076.09	179,076.09	179,076.09	100%	100%	-10
Traffic Signs		52	05-Mar-26	07-May-26	11-May-26 A	31-May-26 A	179,076.09	179,076.09	179,076.09	100%	100%	-17
JDH4-02-007-	PO for Traffic Signs	6	05-Mar-26	11-Mar-26	11-May-26 A	11-May-26 A	0.00	0.00	0.00	100%	100%	-49
JDH4-02-007-	Material Fabrication for Traffic Signs	30	12-Mar-26	19-Apr-26	12-May-26 A	20-May-26 A	0.00	0.00	0.00	100%	100%	-27
JDH4-02-007-	Material Delivery for Traffic Signs	16	20-Apr-26	07-May-26	21-May-26 A	31-May-26 A	179,076.09	179,076.09	179,076.09	100%	100%	-17
Stormwater Utilities		138	27-Dec-25	16-May-26	27-Dec-25 A	17-May-26 A	716,304.35	716,304.35	716,304.35	100%	100%	0
Catch Basins		134	31-Dec-25	16-May-26	31-Dec-25 A	17-Mar-26 A	179,076.09	179,076.09	179,076.09	100%	100%	48
JDH4-02-007-	PO for Catch Basins	3	31-Dec-25	03-Jan-26	31-Dec-25 A	03-Jan-26 A	0.00	0.00	0.00	100%	100%	0
JDH4-02-007-	Material Fabrication for Catch Basins	45	03-Jan-26	24-Feb-26	03-Jan-26 A	01-Feb-26 A	0.00	0.00	0.00	100%	100%	19
JDH4-02-007-	Material Fabrication for Catch Basins	18	19-Feb-26	12-Mar-26	02-Feb-26 A	04-Feb-26 A	0.00	0.00	0.00	100%	100%	30
JDH4-02-007-	Material Fabrication for Catch Basins	30	14-Mar-26	20-Apr-26	04-Feb-26 A	17-Mar-26 A	0.00	0.00	0.00	100%	100%	26
JDH4-02-007-	Material Delivery for Catch Basins(C	3	29-Jan-26	01-Feb-26	29-Jan-26 A	01-Feb-26 A	53,722.83	53,722.83	53,722.83	100%	100%	0
JDH4-02-007-	Material Delivery for Catch Basins	25	29-Mar-26	26-Apr-26	29-Jan-26 A	10-Feb-26 A	125,353.26	125,353.26	125,353.26	100%	100%	60
JDH4-02-007-	Staging Time for Catch Basins	7	09-May-26	16-May-26	28-Feb-26 A	07-Mar-26 A	0.00	0.00	0.00	100%	100%	57
GRP Pipes		100	27-Dec-25	26-Apr-26	27-Dec-25 A	17-Mar-26 A	358,152.18	358,152.18	358,152.18	100%	100%	32
JDH4-02-007-	PO for GRP Pipes	3	27-Dec-25	29-Dec-25	27-Dec-25 A	29-Dec-25 A	0.00	0.00	0.00	100%	100%	0
JDH4-02-007-	Material Fabrication for GRP Pipes	63	27-Dec-25	10-Mar-26	27-Dec-25 A	01-Feb-26 A	0.00	0.00	0.00	100%	100%	31
JDH4-02-007-	Material Fabrication for GRP Pipes	30	14-Feb-26	24-Mar-26	02-Feb-26 A	09-Mar-26 A	0.00	0.00	0.00	100%	100%	11
JDH4-02-007-	Material Delivery for GRP Pipes(Con	32	27-Dec-25	01-Feb-26	27-Dec-25 A	01-Feb-26 A	196,983.70	196,983.70	196,983.70	100%	100%	0
JDH4-02-007-	Material Delivery for GRP Pipes	28	25-Mar-26	26-Apr-26	02-Feb-26 A	17-Mar-26 A	161,168.48	161,168.48	161,168.48	100%	100%	32
Inlet Manholes		70	01-Jan-26	28-Mar-26	01-Jan-26 A	17-May-26 A	179,076.09	179,076.09	179,076.09	100%	100%	-42
JDH4-02-007-	PO for Inlet Manholes	2	01-Jan-26	03-Jan-26	01-Jan-26 A	03-Jan-26 A	0.00	0.00	0.00	100%	100%	0
JDH4-02-007-	Material Fabrication for Inlet Manhole	57	03-Jan-26	10-Mar-26	03-Jan-26 A	01-Feb-26 A	0.00	0.00	0.00	100%	100%	31
JDH4-02-007-	Material Fabrication for Inlet Manhole	30	14-Feb-26	24-Mar-26	02-Feb-26 A	07-May-26 A	0.00	0.00	0.00	100%	100%	-38

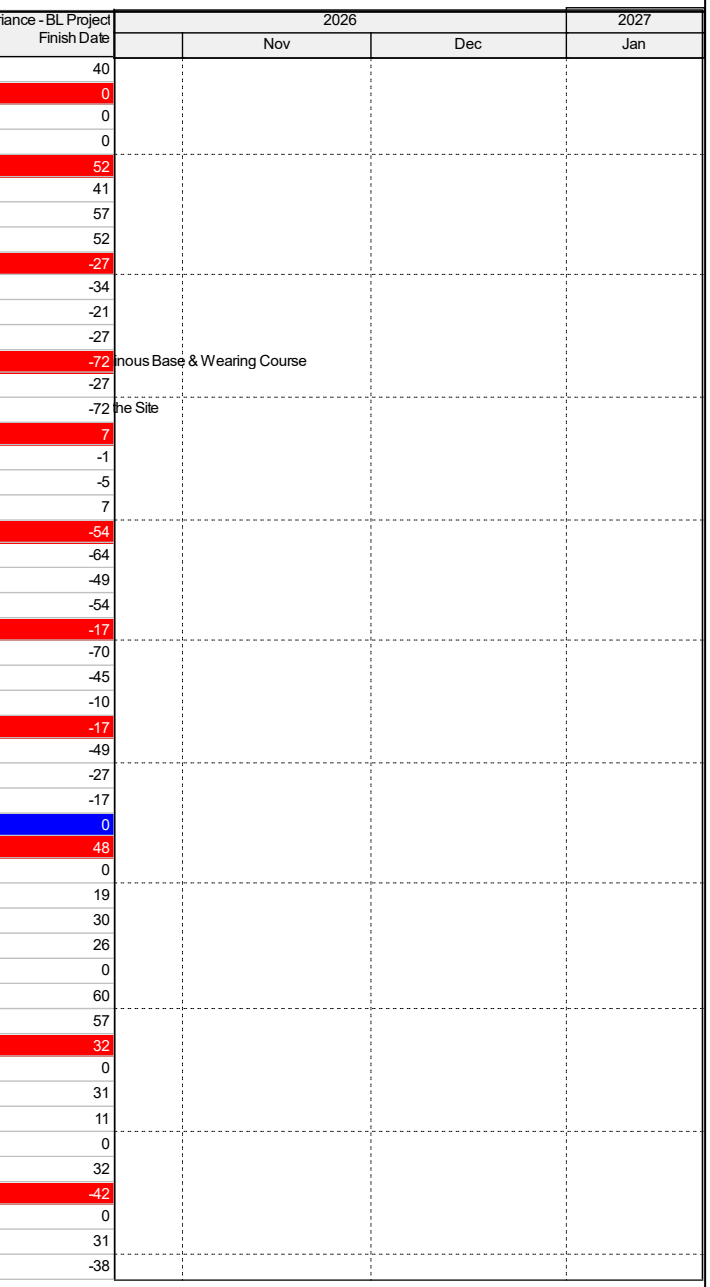


Activity ID	Activity Name	Original Duration	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Schedule % Complete	Performance % Complete	Variance - BL Project Finish Date
JDH4-02-007-	Material Delivery for Inlet Manholes(C	22	07-Jan-26	01-Feb-26	07-Jan-26 A	01-Feb-26 A	71,630.44	71,630.44	71,630.44	100%	100%	0
JDH4-02-007-	Material Delivery for Inlet Manholes	30	17-Feb-26	28-Mar-26	02-Feb-26 A	17-May-26 A	107,445.65	107,445.65	107,445.65	100%	100%	-42
Sanitary Sewerage		108	27-Dec-25	30-Apr-26	27-Dec-25 A	06-May-26 A	716,304.35	716,304.35	716,304.35	100%	100%	-5
GRP Pipes		92	27-Dec-25	16-Apr-26	27-Dec-25 A	25-Mar-26 A	358,152.18	358,152.18	358,152.18	100%	100%	20
JDH4-02-007-	PO for GRP Pipes	3	27-Dec-25	29-Dec-25	27-Dec-25 A	29-Dec-25 A	0.00	0.00	0.00	100%	100%	0
JDH4-02-007-	Material Fabrication for GRP Pipes	60	30-Dec-25	10-Mar-26	30-Dec-25 A	01-Feb-26 A	0.00	0.00	0.00	100%	100%	31
JDH4-02-007-	Material Fabrication for GRP Pipes	30	14-Feb-26	24-Mar-26	02-Feb-26 A	09-Mar-26 A	0.00	0.00	0.00	100%	100%	11
JDH4-02-007-	Material Delivery for GRP Pipes(Con	3	29-Jan-26	01-Feb-26	29-Jan-26 A	01-Feb-26 A	17,907.61	17,907.61	17,907.61	100%	100%	0
JDH4-02-007-	Material Delivery for GRP Pipes	20	25-Mar-26	16-Apr-26	02-Feb-26 A	25-Mar-26 A	340,244.57	340,244.57	340,244.57	100%	100%	20
Manholes		103	01-Jan-26	30-Apr-26	01-Jan-26 A	06-May-26 A	358,152.17	358,152.17	358,152.17	100%	100%	-5
JDH4-02-007-	PO for Manholes	3	01-Jan-26	04-Jan-26	01-Jan-26 A	04-Jan-26 A	0.00	0.00	0.00	100%	100%	0
JDH4-02-007-	Material Fabrication for Manholes - S	5	04-Jan-26	08-Jan-26	04-Jan-26 A	08-Jan-26 A	0.00	0.00	0.00	100%	100%	0
JDH4-02-007-	Material Fabrication for Manholes - S	20	19-Feb-26	15-Mar-26	09-Feb-26 A	11-Mar-26 A	0.00	0.00	0.00	100%	100%	3
JDH4-02-007-	Material Fabrication for Manholes - S	20	16-Mar-26	11-Apr-26	12-Mar-26 A	27-Apr-26 A	0.00	0.00	0.00	100%	100%	-14
JDH4-02-007-	Material Delivery for Manholes(Comp	20	10-Jan-26	01-Feb-26	10-Jan-26 A	01-Feb-26 A	161,168.48	161,168.48	161,168.48	100%	100%	0
JDH4-02-007-	Material Delivery for Manholes	17	12-Apr-26	30-Apr-26	03-Feb-26 A	06-May-26 A	196,983.69	196,983.69	196,983.69	100%	100%	-5
TSE Network		92	01-Jan-26	22-Apr-26	01-Jan-26 A	09-Feb-26 A	179,076.09	179,076.09	179,076.09	100%	100%	58
HDPE Pipe (PN 16)		92	01-Jan-26	22-Apr-26	01-Jan-26 A	09-Feb-26 A	179,076.09	179,076.09	179,076.09	100%	100%	58
JDH4-02-007-	PO for HDPE Pipe (PN 16)	4	01-Jan-26	05-Jan-26	01-Jan-26 A	05-Jan-26 A	0.00	0.00	0.00	100%	100%	0
JDH4-02-007-	Material Fabrication for HDPE Pipe (I	53	01-Jan-26	04-Mar-26	01-Jan-26 A	01-Feb-26 A	0.00	0.00	0.00	100%	100%	26
JDH4-02-007-	Material Fabrication for HDPE Pipe (I	25	14-Feb-26	15-Mar-26	02-Feb-26 A	03-Feb-26 A	0.00	0.00	0.00	100%	100%	33
JDH4-02-007-	Material Delivery for HDPE Pipe (PN	26	03-Jan-26	01-Feb-26	03-Jan-26 A	01-Feb-26 A	164,750.00	164,750.00	164,750.00	100%	100%	0
JDH4-02-007-	Material Delivery for HDPE Pipe (PN	30	16-Mar-26	22-Apr-26	02-Feb-26 A	09-Feb-26 A	14,326.09	14,326.09	14,326.09	100%	100%	58
Potable Water Network		90	01-Jan-26	12-Apr-26	01-Jan-26 A	09-Feb-26 A	179,076.09	179,076.09	179,076.09	100%	100%	49
HDPE Pipe (PN 16)		90	01-Jan-26	12-Apr-26	01-Jan-26 A	09-Feb-26 A	179,076.09	179,076.09	179,076.09	100%	100%	49
JDH4-02-007-	PO for HDPE Pipe (PN 16)	2	01-Jan-26	03-Jan-26	01-Jan-26 A	03-Jan-26 A	0.00	0.00	0.00	100%	100%	0
JDH4-02-007-	Material Fabrication for HDPE Pipe (I	52	03-Jan-26	04-Mar-26	03-Jan-26 A	01-Feb-26 A	0.00	0.00	0.00	100%	100%	26
JDH4-02-007-	Material Fabrication for HDPE Pipe (I	25	03-Feb-26	04-Mar-26	02-Feb-26 A	03-Feb-26 A	0.00	0.00	0.00	100%	100%	24
JDH4-02-007-	Material Delivery for HDPE Pipe (PN	26	03-Jan-26	01-Feb-26	03-Jan-26 A	01-Feb-26 A	148,633.15	148,633.15	148,633.15	100%	100%	0
JDH4-02-007-	Material Delivery for HDPE Pipe (PN	30	05-Mar-26	12-Apr-26	02-Feb-26 A	09-Feb-26 A	30,442.94	30,442.94	30,442.94	100%	100%	49
Electrical Network		121	15-Feb-26	24-May-26	01-Feb-26 A	23-Apr-26 A	358,152.04	358,152.04	358,152.04	100%	100%	26
Pipe for the Duct		61	15-Feb-26	30-Apr-26	01-Feb-26 A	22-Apr-26 A	179,075.95	179,075.95	179,075.95	100%	100%	7
JDH4-02-007-	PO for Pipe for Duct	6	15-Feb-26	21-Feb-26	01-Feb-26 A	04-Feb-26 A	0.00	0.00	0.00	100%	100%	14
JDH4-02-007-	Material Fabrication for Pipe for Duct	30	23-Feb-26	01-Apr-26	05-Feb-26 A	09-Apr-26 A	0.00	0.00	0.00	100%	100%	-6
JDH4-02-007-	Material Delivery for Pipe for Duct	25	02-Apr-26	30-Apr-26	11-Feb-26 A	22-Apr-26 A	179,075.95	179,075.95	179,075.95	100%	100%	7
Earthing System		76	25-Feb-26	24-May-26	18-Mar-26 A	23-Apr-26 A	179,076.09	179,076.09	179,076.09	100%	100%	26
JDH4-02-007-	PO for Earthing System	7	25-Feb-26	04-Mar-26	18-Mar-26 A	22-Mar-26 A	0.00	0.00	0.00	100%	100%	-12
JDH4-02-007-	Material Fabrication for Earthing Syst	30	05-Mar-26	12-Apr-26	23-Mar-26 A	26-Mar-26 A	0.00	0.00	0.00	100%	100%	14
JDH4-02-007-	Material Delivery for Earthing System	28	22-Apr-26	24-May-26	29-Mar-26 A	23-Apr-26 A	179,076.09	179,076.09	179,076.09	100%	100%	26
Telecommunications		96	20-Jan-26	16-May-26	20-Jan-26 A	08-Feb-26 A	179,076.09	179,076.09	179,076.09	100%	100%	79
Pipe for the Duct		96	20-Jan-26	16-May-26	20-Jan-26 A	08-Feb-26 A	179,076.09	179,076.09	179,076.09	100%	100%	79
JDH4-02-007-	PO for Pipe for Duct	2	20-Jan-26	21-Jan-26	20-Jan-26 A	21-Jan-26 A	0.00	0.00	0.00	100%	100%	0
JDH4-02-007-	Material Fabrication for Pipe for Duct	8	25-Jan-26	02-Feb-26	25-Jan-26 A	01-Feb-26 A	0.00	0.00	0.00	100%	100%	2
JDH4-02-007-	Material Fabrication for Pipe for Duct	10	02-Apr-26	13-Apr-26	02-Feb-26 A	04-Feb-26 A	0.00	0.00	0.00	100%	100%	54
JDH4-02-007-	Material Delivery for Pipe for Duct(Co	2	31-Jan-26	01-Feb-26	31-Jan-26 A	01-Feb-26 A	71,630.44	71,630.44	71,630.44	100%	100%	0
JDH4-02-007-	Material Delivery for Pipe for Duct	28	13-Apr-26	16-May-26	02-Feb-26 A	08-Feb-26 A	107,445.65	107,445.65	107,445.65	100%	100%	79
Sewage Lift Station		222	03-Feb-26	01-Sep-26	02-Feb-26 A	12-Aug-26 A	1,253,532.63	1,253,532.63	1,253,532.63	100%	100%	17
Thermal & Moisture Protection		121	11-Mar-26	05-Aug-26	04-Mar-26 A	18-Apr-26 A	179,076.09	179,076.09	179,076.09	100%	100%	91
JDH4-02-007-	PO for Thermal & Moisture Protectior	4	11-Mar-26	15-Mar-26	04-Mar-26 A	12-Mar-26 A	0.00	0.00	0.00	100%	100%	2
JDH4-02-007-	Material Fabrication for Thermal & Mc	20	16-Mar-26	11-Apr-26	14-Mar-26 A	16-Mar-26 A	0.00	0.00	0.00	100%	100%	19
JDH4-02-007-	Material Fabrication for Thermal & Mc	20	12-Apr-26	04-May-26	17-Mar-26 A	19-Mar-26 A	0.00	0.00	0.00	100%	100%	38

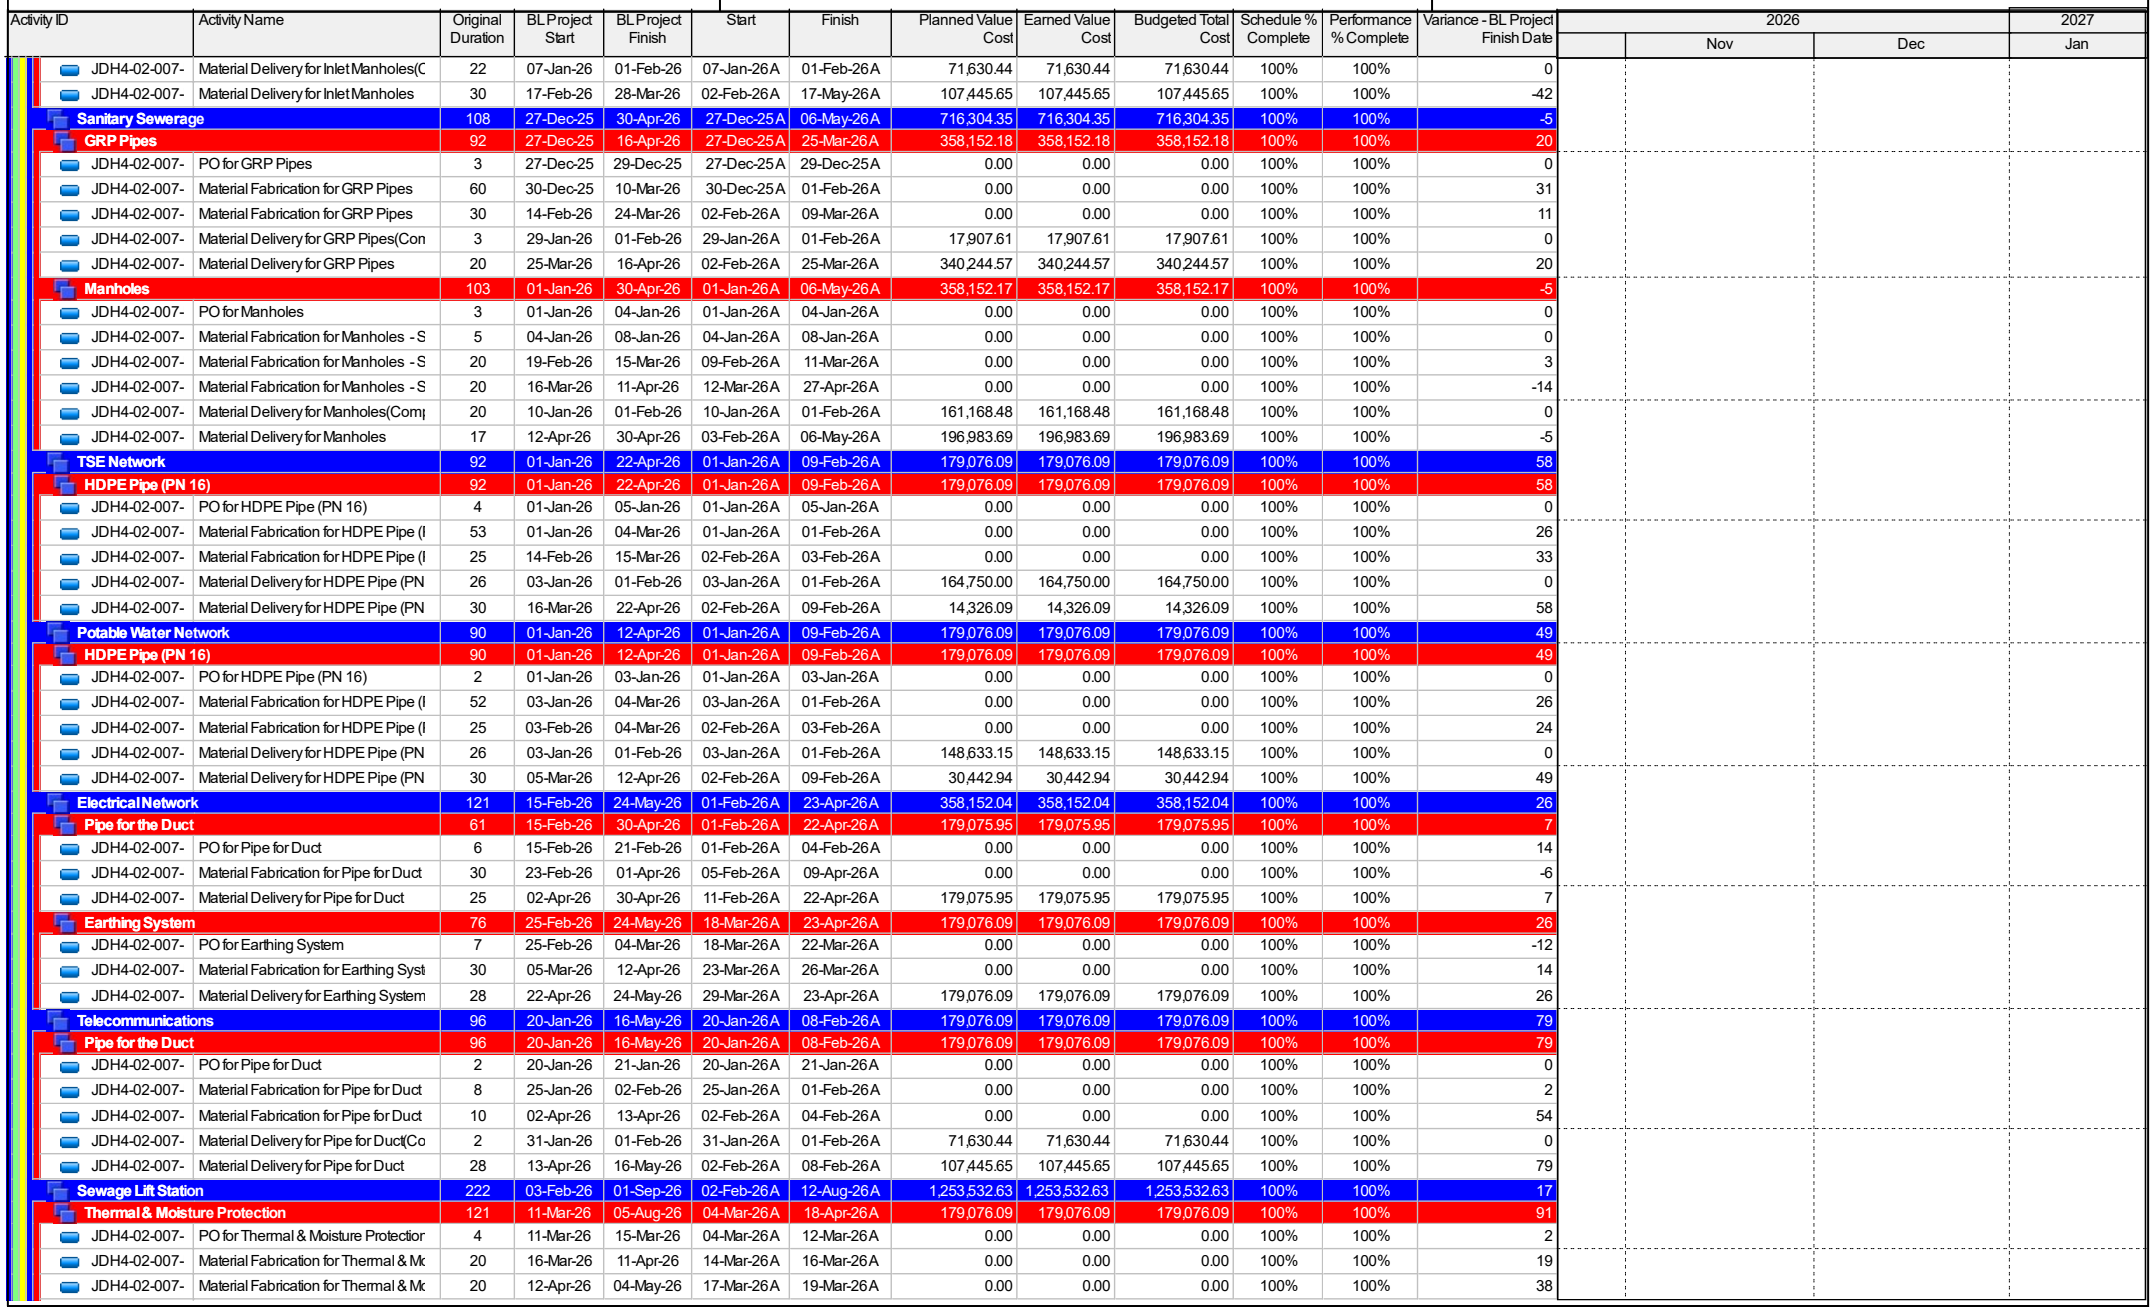

Date	Revision	Checked	Approved

Activity ID	Activity Name	Original Duration	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Schedule % Complete	Performance % Complete	Variance - BL Project Finish Date
JDH4-02-007-	Material Fabrication for Thermal & Mc	29	05-May-26	10-Jun-26	21-Mar-26 A	25-Mar-26 A	0.00	0.00	0.00	100%	100%	63
JDH4-02-007-	Material Delivery for Thermal & Moist	24	11-Jun-26	08-Jul-26	30-Mar-26 A	05-Apr-26 A	0.00	0.00	0.00	100%	100%	78
JDH4-02-007-	Material Delivery for Thermal & Moist	24	09-Jul-26	05-Aug-26	06-Apr-26 A	18-Apr-26 A	179,076.09	179,076.09	179,076.09	100%	100%	91
Metals		132	11-Mar-26	05-Aug-26	03-Mar-26 A	24-Jun-26 A	179,076.09	179,076.09	179,076.09	100%	100%	36
JDH4-02-007-	PO for Metal	4	11-Mar-26	15-Mar-26	03-Mar-26 A	11-Mar-26 A	0.00	0.00	0.00	100%	100%	3
JDH4-02-007-	Material Fabrication for Metal - Stage	29	16-Mar-26	21-Apr-26	12-Mar-26 A	09-Apr-26 A	0.00	0.00	0.00	100%	100%	10
JDH4-02-007-	Material Fabrication for Metal - Stage	20	22-Apr-26	14-May-26	11-Apr-26 A	23-Apr-26 A	0.00	0.00	0.00	100%	100%	18
JDH4-02-007-	Material Fabrication for Metal - Stage	20	16-May-26	10-Jun-26	25-Apr-26 A	07-May-26 A	0.00	0.00	0.00	100%	100%	26
JDH4-02-007-	Material Delivery for Metal - Stage 1	18	11-Jun-26	01-Jul-26	11-Jun-26 A	24-Jun-26 A	0.00	0.00	0.00	100%	100%	6
JDH4-02-007-	Material Delivery for Metal - Stage 2	30	02-Jul-26	05-Aug-26	11-Jun-26 A	24-Jun-26 A	179,076.09	179,076.09	179,076.09	100%	100%	36
Pipes		85	03-Feb-26	20-Apr-26	02-Feb-26 A	18-Apr-26 A	179,076.09	179,076.09	179,076.09	100%	100%	2
JDH4-02-007-	PO for Pipes	4	03-Feb-26	07-Feb-26	02-Feb-26 A	04-Feb-26 A	0.00	0.00	0.00	100%	100%	2
JDH4-02-007-	Material Fabrication for Pipes	30	08-Feb-26	15-Mar-26	11-Feb-26 A	15-Apr-26 A	0.00	0.00	0.00	100%	100%	-24
JDH4-02-007-	Material Delivery for Pipes	28	16-Mar-26	20-Apr-26	12-Apr-26 A	18-Apr-26 A	179,076.09	179,076.09	179,076.09	100%	100%	2
Air Conditioning and Ventilation		99	19-Feb-26	23-May-26	04-Mar-26 A	19-Apr-26 A	179,076.09	179,076.09	179,076.09	100%	100%	29
JDH4-02-007-	PO for Air Conditioning and Ventilatic	4	19-Feb-26	24-Feb-26	04-Mar-26 A	11-Mar-26 A	0.00	0.00	0.00	100%	100%	-13
JDH4-02-007-	Material Fabrication for Air Conditioni	30	25-Feb-26	04-Apr-26	12-Mar-26 A	15-Apr-26 A	0.00	0.00	0.00	100%	100%	-10
JDH4-02-007-	Material Delivery for Air Conditioning	28	21-Apr-26	23-May-26	14-Apr-26 A	19-Apr-26 A	179,076.09	179,076.09	179,076.09	100%	100%	29
Fuel System		62	08-Mar-26	28-Jun-26	15-Jul-26 A	12-Aug-26 A	179,076.09	179,076.09	179,076.09	100%	100%	-39
JDH4-02-007-	PO for Fabrication for Fuel System	4	08-Mar-26	11-Mar-26	15-Jul-26 A	16-Jul-26 A	0.00	0.00	0.00	100%	100%	-103
JDH4-02-007-	Material Fabrication for Fuel System	30	12-Mar-26	19-Apr-26	18-Jul-26 A	05-Aug-26 A	0.00	0.00	0.00	100%	100%	-90
JDH4-02-007-	Material Delivery for Fuel System	28	24-May-26	28-Jun-26	10-Aug-26 A	12-Aug-26 A	179,076.09	179,076.09	179,076.09	100%	100%	-39
Fire Fighting System		90	11-Mar-26	30-Jul-26	15-Jul-26 A	12-Aug-26 A	179,076.09	179,076.09	179,076.09	100%	100%	-11
JDH4-02-007-	PO for Fire Fighting System	4	11-Mar-26	15-Mar-26	15-Jul-26 A	16-Jul-26 A	0.00	0.00	0.00	100%	100%	-100
JDH4-02-007-	Material Fabrication for Fire Fighting S	30	16-Mar-26	22-Apr-26	18-Jul-26 A	06-Aug-26 A	0.00	0.00	0.00	100%	100%	-88
JDH4-02-007-	Material Delivery for Fire Fighting Sys	28	29-Jun-26	30-Jul-26	10-Aug-26 A	12-Aug-26 A	179,076.09	179,076.09	179,076.09	100%	100%	-11
Security System (CCTV System)		136	23-Apr-26	01-Sep-26	28-Feb-26 A	11-Apr-26 A	179,076.09	179,076.09	179,076.09	100%	100%	120
JDH4-02-007-	PO for Security System (CCTV Syste	4	23-Apr-26	27-Apr-26	28-Feb-26 A	02-Mar-26 A	0.00	0.00	0.00	100%	100%	45
JDH4-02-007-	Material Fabrication for Security Syste	30	28-Apr-26	04-Jun-26	03-Mar-26 A	25-Mar-26 A	0.00	0.00	0.00	100%	100%	58
JDH4-02-007-	Material Delivery for Security System	28	01-Aug-26	01-Sep-26	02-Apr-26 A	11-Apr-26 A	179,076.09	179,076.09	179,076.09	100%	100%	120
Long Lead Item		341	28-Jan-26	31-Dec-26	25-Jan-26 A	06-Oct-26 A	4,988,121.85	6,267,663.15	6,267,663.15	79.59%	100%	74
TSE Network		116	15-Feb-26	28-Jun-26	23-Feb-26 A	04-May-26 A	358,152.18	358,152.18	358,152.18	100%	100%	44
Valves / Chambers		108	15-Feb-26	28-Jun-26	23-Feb-26 A	31-Mar-26 A	179,076.09	179,076.09	179,076.09	100%	100%	73
JDH4-02-007-	PO for Valves / Chambers	5	15-Feb-26	19-Feb-26	23-Feb-26 A	25-Feb-26 A	0.00	0.00	0.00	100%	100%	-4
JDH4-02-007-	Material Fabrication for Valves / Char	8	21-Feb-26	02-Mar-26	25-Feb-26 A	28-Feb-26 A	0.00	0.00	0.00	100%	100%	2
JDH4-02-007-	Material Fabrication for Valves / Char	30	03-Mar-26	09-Apr-26	26-Feb-26 A	01-Mar-26 A	0.00	0.00	0.00	100%	100%	31
JDH4-02-007-	Material Fabrication for Valves / Char	20	11-Apr-26	03-May-26	28-Feb-26 A	04-Mar-26 A	0.00	0.00	0.00	100%	100%	48
JDH4-02-007-	Material Fabrication for Valves / Char	20	04-May-26	30-May-26	04-Mar-26 A	07-Mar-26 A	0.00	0.00	0.00	100%	100%	66
JDH4-02-007-	Material Delivery for Valves / Chambe	18	31-May-26	20-Jun-26	15-Mar-26 A	26-Mar-26 A	179,076.09	179,076.09	179,076.09	100%	100%	70
JDH4-02-007-	Staging Time for Valves / Chambers	7	21-Jun-26	28-Jun-26	28-Mar-26 A	31-Mar-26 A	0.00	0.00	0.00	100%	100%	73
Risers		65	17-Feb-26	16-May-26	01-Mar-26 A	04-May-26 A	179,076.09	179,076.09	179,076.09	100%	100%	10
JDH4-02-007-	PO for Risers	5	17-Feb-26	23-Feb-26	01-Mar-26 A	04-Mar-26 A	0.00	0.00	0.00	100%	100%	-8
JDH4-02-007-	Material Fabrication for Risers - Stag	12	24-Feb-26	09-Mar-26	05-Mar-26 A	14-Mar-26 A	0.00	0.00	0.00	100%	100%	-4
JDH4-02-007-	Material Fabrication for Risers - Stag	12	10-Mar-26	26-Mar-26	15-Mar-26 A	22-Mar-26 A	0.00	0.00	0.00	100%	100%	4
JDH4-02-007-	Material Fabrication for Risers - Stag	12	28-Mar-26	09-Apr-26	23-Mar-26 A	25-Mar-26 A	0.00	0.00	0.00	100%	100%	13
JDH4-02-007-	Material Fabrication for Risers - Stag	12	11-Apr-26	23-Apr-26	29-Mar-26 A	31-Mar-26 A	0.00	0.00	0.00	100%	100%	20
JDH4-02-007-	Material Delivery for Risers	12	25-Apr-26	07-May-26	01-Apr-26 A	30-Apr-26 A	179,076.09	179,076.09	179,076.09	100%	100%	6
JDH4-02-007-	Staging Time for Risers	7	09-May-26	16-May-26	02-May-26 A	04-May-26 A	0.00	0.00	0.00	100%	100%	10
Potable Water Network		135	21-Feb-26	13-Aug-26	02-Feb-26 A	04-Apr-26 A	358,152.18	358,152.18	358,152.18	100%	100%	110
Valves / Chambers		52	21-Feb-26	28-Apr-26	08-Feb-26 A	31-Mar-26 A	179,076.09	179,076.09	179,076.09	100%	100%	24

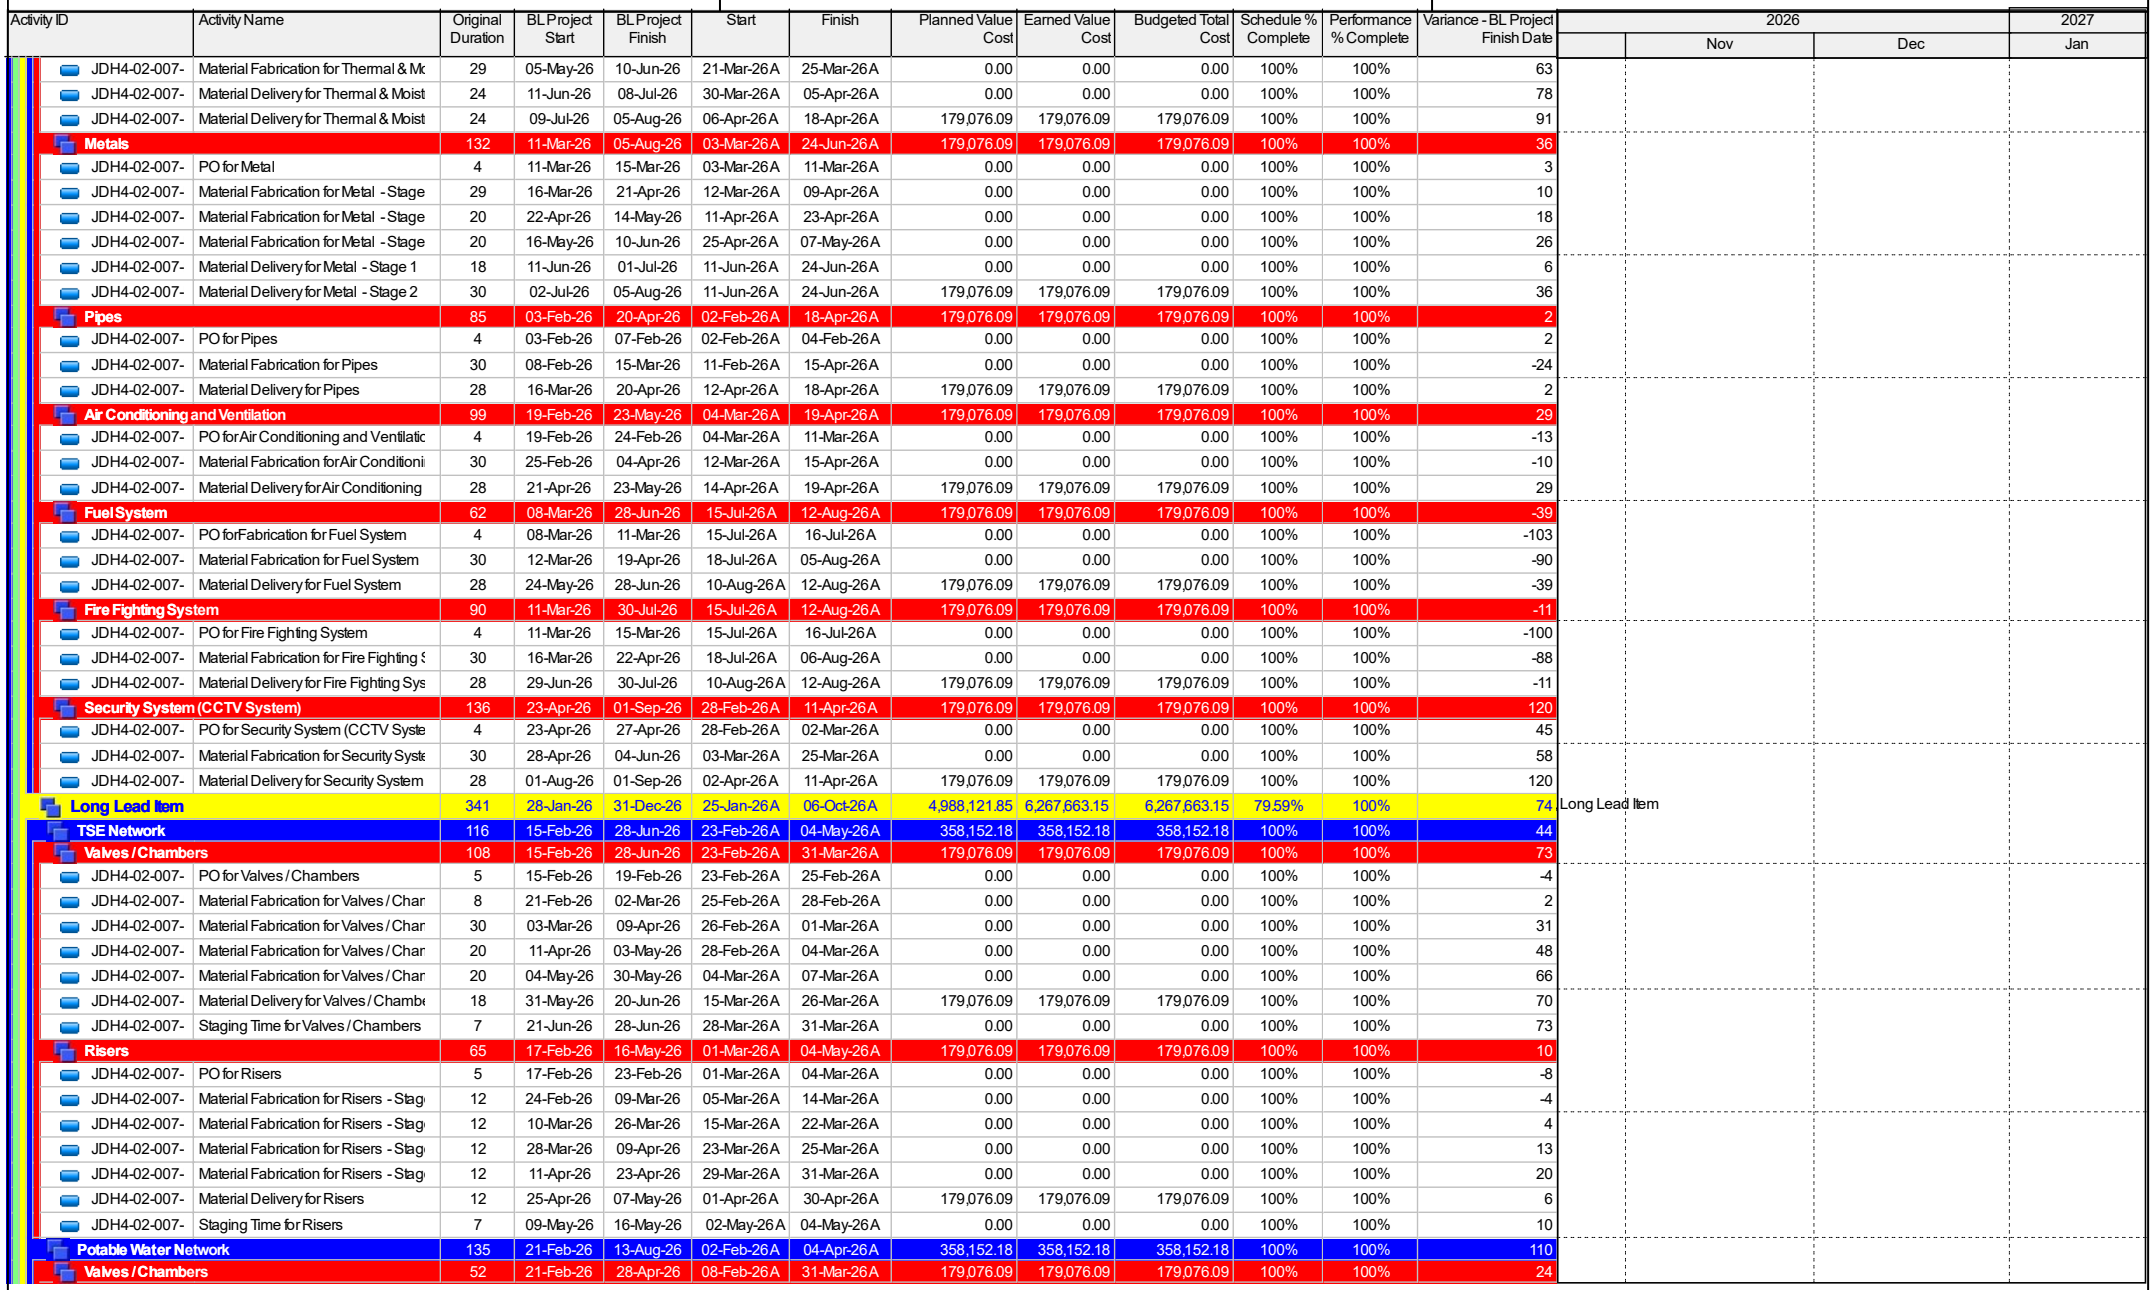

Actual Work
Remaining Work
Critical Remaining Work
Milestone


Date	Revision	Checked	Approved

Activity ID	Activity Name	Original Duration	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Schedule % Complete	Performance % Complete	Variance - BL Project Finish Date
JDH4-02-007-	PO for Valves / Chambers	5	21-Feb-26	26-Feb-26	08-Feb-26 A	10-Feb-26 A	0.00	0.00	0.00	100%	100%	13
JDH4-02-007-	Material Fabrication for Valves / Char	10	28-Feb-26	10-Mar-26	11-Feb-26 A	12-Feb-26 A	0.00	0.00	0.00	100%	100%	21
JDH4-02-007-	Material Fabrication for Valves / Char	10	11-Mar-26	25-Mar-26	11-Feb-26 A	14-Feb-26 A	0.00	0.00	0.00	100%	100%	30
JDH4-02-007-	Material Fabrication for Valves / Char	10	29-Mar-26	08-Apr-26	12-Feb-26 A	17-Feb-26 A	0.00	0.00	0.00	100%	100%	39
JDH4-02-007-	Material Delivery for Valves / Chambe	10	09-Apr-26	20-Apr-26	23-Feb-26 A	21-Mar-26 A	179,076.09	179,076.09	179,076.09	100%	100%	26
JDH4-02-007-	Staging Time for Valves / Chambers	7	21-Apr-26	28-Apr-26	25-Mar-26 A	31-Mar-26 A	0.00	0.00	0.00	100%	100%	24
Fire Hydrants		135	21-Feb-26	13-Aug-26	02-Feb-26 A	04-Apr-26 A	179,076.09	179,076.09	179,076.09	100%	100%	110
JDH4-02-007-	PO for Fire Hydrant	5	21-Feb-26	26-Feb-26	02-Feb-26 A	10-Feb-26 A	0.00	0.00	0.00	100%	100%	13
JDH4-02-007-	Material Fabrication for Fire Hydrant	30	28-Feb-26	06-Apr-26	11-Feb-26 A	14-Feb-26 A	0.00	0.00	0.00	100%	100%	40
JDH4-02-007-	Material Fabrication for Fire Hydrant	20	07-Apr-26	29-Apr-26	15-Feb-26 A	17-Feb-26 A	0.00	0.00	0.00	100%	100%	57
JDH4-02-007-	Material Fabrication for Fire Hydrant	20	30-Apr-26	23-May-26	18-Feb-26 A	21-Feb-26 A	0.00	0.00	0.00	100%	100%	74
JDH4-02-007-	Material Fabrication for Fire Hydrant	25	24-May-26	24-Jun-26	22-Feb-26 A	25-Feb-26 A	0.00	0.00	0.00	100%	100%	96
JDH4-02-007-	Material Delivery for Fire Hydrant	25	25-Jun-26	23-Jul-26	25-Feb-26 A	30-Mar-26 A	179,076.09	179,076.09	179,076.09	100%	100%	96
JDH4-02-007-	Staging Time for Fire Hydrant	7	06-Aug-26	13-Aug-26	31-Mar-26 A	04-Apr-26 A	0.00	0.00	0.00	100%	100%	110
Electrical Network		243	03-Feb-26	31-Dec-26	17-Feb-26 A	06-Aug-26 A	1,253,532.63	1,432,608.72	1,432,608.72	87.5%	100%	125
Medium Voltage Cable		69	14-Nov-26	31-Dec-26	20-Apr-26 A	15-Jun-26 A	0.00	179,076.09	179,076.09	0%	100%	170
JDH4-02-007-	PO for Medium Voltage Cable	7	14-Nov-26	21-Nov-26	20-Apr-26 A	21-Apr-26 A	0.00	0.00	0.00	0%	100%	179
JDH4-02-007-	Material Fabrication for Medium Volta	25	22-Nov-26	20-Dec-26	26-Apr-26 A	30-Apr-26 A	0.00	0.00	0.00	0%	100%	197
JDH4-02-007-	Material Fabrication for Medium Volta	25	22-Nov-26	20-Dec-26	22-Apr-26 A	26-Apr-26 A	0.00	0.00	0.00	0%	100%	200
JDH4-02-007-	Material Delivery for Medium Voltage	10	21-Dec-26	31-Dec-26	28-Apr-26 A	13-Jun-26 A	0.00	179,076.09	179,076.09	0%	100%	172
JDH4-02-007-	Staging Time for Medium Voltage Ca	10	21-Dec-26	31-Dec-26	14-Jun-26 A	15-Jun-26 A	0.00	0.00	0.00	0%	100%	170
Unit Sub Station		114	25-Feb-26	20-Aug-26	07-Jun-26 A	29-Jul-26 A	179,076.09	179,076.09	179,076.09	100%	100%	19
JDH4-02-007-	PO for Unit Sub-station	19	25-Feb-26	22-Mar-26	07-Jun-26 A	08-Jun-26 A	0.00	0.00	0.00	100%	100%	-64
JDH4-02-007-	Material Fabrication for Unit Sub-stati	5	23-Mar-26	28-Mar-26	09-Jun-26 A	13-Jun-26 A	0.00	0.00	0.00	100%	100%	-63
JDH4-02-007-	Material Fabrication for Unit Sub-stati	30	29-Mar-26	02-May-26	14-Jun-26 A	15-Jun-26 A	0.00	0.00	0.00	100%	100%	-35
JDH4-02-007-	Material Fabrication for Unit Sub-stati	30	03-May-26	09-Jun-26	16-Jun-26 A	20-Jun-26 A	0.00	0.00	0.00	100%	100%	-9
JDH4-02-007-	Material Fabrication for Unit Sub-stati	30	10-Jun-26	14-Jul-26	21-Jun-26 A	23-Jun-26 A	0.00	0.00	0.00	100%	100%	18
JDH4-02-007-	Material Delivery for Unit Sub-station	25	15-Jul-26	12-Aug-26	25-Jul-26 A	27-Jul-26 A	179,076.09	179,076.09	179,076.09	100%	100%	14
JDH4-02-007-	Staging Time for Unit Sub-station	7	13-Aug-26	20-Aug-26	28-Jul-26 A	29-Jul-26 A	0.00	0.00	0.00	100%	100%	19
Low Voltage Cables		131	03-Feb-26	10-Jun-26	22-Feb-26 A	09-May-26 A	179,076.09	179,076.09	179,076.09	100%	100%	25
JDH4-02-007-	PO for Low Voltage Cables	7	03-Feb-26	10-Feb-26	22-Feb-26 A	25-Feb-26 A	0.00	0.00	0.00	100%	100%	-12
JDH4-02-007-	Material Fabrication for Low Voltage (	11	11-Feb-26	24-Feb-26	26-Feb-26 A	11-Apr-26 A	0.00	0.00	0.00	100%	100%	-36
JDH4-02-007-	Material Fabrication for Low Voltage (	25	25-Feb-26	29-Mar-26	12-Apr-26 A	20-Apr-26 A	0.00	0.00	0.00	100%	100%	-19
JDH4-02-007-	Material Fabrication for Low Voltage (	25	30-Mar-26	27-Apr-26	21-Apr-26 A	23-Apr-26 A	0.00	0.00	0.00	100%	100%	3
JDH4-02-007-	Material Delivery for Low Voltage Cal	28	28-Apr-26	02-Jun-26	22-Apr-26 A	07-May-26 A	179,076.09	179,076.09	179,076.09	100%	100%	19
JDH4-02-007-	Staging Time for Low Voltage Cables	7	03-Jun-26	10-Jun-26	09-May-26 A	09-May-26 A	0.00	0.00	0.00	100%	100%	25
Ring Main Unit		78	28-Feb-26	23-Jul-26	23-Apr-26 A	27-Jun-26 A	179,076.09	179,076.09	179,076.09	100%	100%	23
JDH4-02-007-	PO for Ring Main Unit	5	28-Feb-26	04-Mar-26	23-Apr-26 A	23-Apr-26 A	0.00	0.00	0.00	100%	100%	-40
JDH4-02-007-	Material Fabrication for Ring Main Ur	25	05-Mar-26	06-Apr-26	24-Apr-26 A	02-May-26 A	0.00	0.00	0.00	100%	100%	-22
JDH4-02-007-	Material Fabrication for Ring Main Ur	25	07-Apr-26	05-May-26	03-May-26 A	16-May-26 A	0.00	0.00	0.00	100%	100%	-9
JDH4-02-007-	Material Fabrication for Ring Main Ur	25	06-May-26	07-Jun-26	16-May-26 A	31-May-26 A	0.00	0.00	0.00	100%	100%	6
JDH4-02-007-	Material Delivery for Ring Main Unit	28	08-Jun-26	09-Jul-26	01-Jun-26 A	23-Jun-26 A	179,076.09	179,076.09	179,076.09	100%	100%	14
JDH4-02-007-	Staging Time for Ring Main Unit	12	11-Jul-26	23-Jul-26	24-Jun-26 A	27-Jun-26 A	0.00	0.00	0.00	100%	100%	23
Lighting poles		159	05-Mar-26	19-Aug-26	17-Feb-26 A	30-Apr-26 A	179,076.09	179,076.09	179,076.09	100%	100%	93
JDH4-02-007-	PO for Lighting poles	4	05-Mar-26	09-Mar-26	17-Feb-26 A	19-Feb-26 A	0.00	0.00	0.00	100%	100%	14
JDH4-02-007-	Material Fabrication for Lighting poles	11	10-Mar-26	25-Mar-26	21-Feb-26 A	11-Mar-26 A	0.00	0.00	0.00	100%	100%	9
JDH4-02-007-	Material Fabrication for Lighting poles	25	26-Mar-26	23-Apr-26	21-Mar-26 A	16-Apr-26 A	0.00	0.00	0.00	100%	100%	7
JDH4-02-007-	Material Fabrication for Lighting poles	25	25-Apr-26	23-May-26	21-Mar-26 A	21-Apr-26 A	0.00	0.00	0.00	100%	100%	28
JDH4-02-007-	Material Delivery for Lighting poles	28	11-Jul-26	11-Aug-26	25-Mar-26 A	29-Apr-26 A	179,076.09	179,076.09	179,076.09	100%	100%	87
JDH4-02-007-	Staging Time for Lighting poles	7	12-Aug-26	19-Aug-26	28-Mar-26 A	30-Apr-26 A	0.00	0.00	0.00	100%	100%	93

2026		2027
Nov	Dec	Jan


Date	Revision	Checked	Approved

Activity ID	Activity Name	Original Duration	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Schedule % Complete	Performance % Complete	Variance - BL Project Finish Date
Street Lighting Luminaire		167	10-Mar-26	02-Sep-26	17-Feb-26 A	25-May-26 A	179,076.09	179,076.09	179,076.09	100%	100%	83
JDH4-02-007-	PO for Street Lighting Luminaire	7	10-Mar-26	17-Mar-26	17-Feb-26 A	19-Feb-26 A	0.00	0.00	0.00	100%	100%	21
JDH4-02-007-	Material Fabrication for Street Lighting	25	22-Mar-26	19-Apr-26	21-Feb-26 A	14-Mar-26 A	0.00	0.00	0.00	100%	100%	29
JDH4-02-007-	Material Fabrication for Street Lighting	25	20-Apr-26	18-May-26	18-Mar-26 A	09-Apr-26 A	0.00	0.00	0.00	100%	100%	34
JDH4-02-007-	Material Fabrication for Street Lighting	25	19-May-26	20-Jun-26	19-Mar-26 A	21-May-26 A	0.00	0.00	0.00	100%	100%	22
JDH4-02-007-	Material Delivery for Street Lighting L	28	21-Jun-26	22-Jul-26	25-Mar-26 A	25-May-26 A	179,076.09	179,076.09	179,076.09	100%	100%	47
JDH4-02-007-	Staging Time for Street Lighting Lumi	12	20-Aug-26	02-Sep-26	26-Mar-26 A	25-May-26 A	0.00	0.00	0.00	100%	100%	83
Lighting panels/Feeder Pillers		113	08-Mar-26	27-Aug-26	30-Apr-26 A	09-Jun-26 A	179,076.09	179,076.09	179,076.09	100%	100%	68
JDH4-02-007-	PO for Lighting Panels/Feeder Pillers	4	08-Mar-26	11-Mar-26	30-Apr-26 A	14-May-26 A	0.00	0.00	0.00	100%	100%	-52
JDH4-02-007-	Material Fabrication for Lighting Pane	25	12-Mar-26	13-Apr-26	16-May-26 A	07-Jun-26 A	0.00	0.00	0.00	100%	100%	-44
JDH4-02-007-	Material Fabrication for Lighting Pane	25	14-Apr-26	12-May-26	08-Jun-26 A	09-Jun-26 A	0.00	0.00	0.00	100%	100%	-21
JDH4-02-007-	Material Fabrication for Lighting Pane	25	13-May-26	14-Jun-26	08-Jun-26 A	09-Jun-26 A	0.00	0.00	0.00	100%	100%	4
JDH4-02-007-	Material Delivery for Lighting Panels/	28	15-Jun-26	16-Jul-26	08-Jun-26 A	09-Jun-26 A	179,076.09	179,076.09	179,076.09	100%	100%	32
JDH4-02-007-	Staging Time for Lighting Panels/Fee	7	20-Aug-26	27-Aug-26	09-Jun-26 A	09-Jun-26 A	0.00	0.00	0.00	100%	100%	68
Low Voltage Distribution Panels		116	12-Mar-26	05-Sep-26	30-Apr-26 A	06-Aug-26 A	179,076.09	179,076.09	179,076.09	100%	100%	25
JDH4-02-007-	PO for Low Voltage Distribution Pane	7	12-Mar-26	23-Mar-26	30-Apr-26 A	14-May-26 A	0.00	0.00	0.00	100%	100%	-45
JDH4-02-007-	Material Fabrication for Low Voltage D	21	24-Mar-26	16-Apr-26	16-May-26 A	23-May-26 A	0.00	0.00	0.00	100%	100%	-31
JDH4-02-007-	Material Fabrication for Low Voltage D	20	18-Apr-26	10-May-26	24-May-26 A	01-Jun-26 A	0.00	0.00	0.00	100%	100%	-16
JDH4-02-007-	Material Fabrication for Low Voltage D	20	11-May-26	06-Jun-26	02-Jun-26 A	30-Jul-26 A	0.00	0.00	0.00	100%	100%	-47
JDH4-02-007-	Material Delivery for Low Voltage Dis	28	07-Jun-26	08-Jul-26	01-Aug-26 A	05-Aug-26 A	179,076.09	179,076.09	179,076.09	100%	100%	-24
JDH4-02-007-	Staging Time for Low Voltage Distribu	7	29-Aug-26	05-Sep-26	06-Aug-26 A	06-Aug-26 A	0.00	0.00	0.00	100%	100%	25
Sewage Lift Station		341	28-Jan-26	24-Dec-26	25-Jan-26 A	06-Oct-26 A	3,018,284.86	4,118,750.07	4,118,750.07	73.28%	100%	68
Odours scrubbing system		129	11-Mar-26	26-Aug-26	08-Feb-26 A	10-Aug-26 A	179,076.09	179,076.09	179,076.09	100%	100%	14
JDH4-02-007-	PO for Odours scrubbing system	4	11-Mar-26	15-Mar-26	08-Feb-26 A	10-Feb-26 A	0.00	0.00	0.00	100%	100%	27
JDH4-02-007-	Material Fabrication for Odours scrub	25	16-Mar-26	16-Apr-26	11-Feb-26 A	14-Feb-26 A	0.00	0.00	0.00	100%	100%	49
JDH4-02-007-	Material Fabrication for Odours scrub	25	18-Apr-26	16-May-26	15-Feb-26 A	18-Feb-26 A	0.00	0.00	0.00	100%	100%	70
JDH4-02-007-	Material Fabrication for Odours scrub	25	17-May-26	17-Jun-26	25-Apr-26 A	10-Jun-26 A	0.00	0.00	0.00	100%	100%	6
JDH4-02-007-	Material Fabrication for Odours scrub	25	18-Jun-26	16-Jul-26	11-Jun-26 A	21-Jun-26 A	0.00	0.00	0.00	100%	100%	22
JDH4-02-007-	Material Delivery for Odours scrubbir	28	18-Jul-26	18-Aug-26	22-Jun-26 A	25-Jun-26 A	179,076.09	179,076.09	179,076.09	100%	100%	46
JDH4-02-007-	Staging Time for Odours scrubbing s	7	19-Aug-26	26-Aug-26	10-Aug-26 A	10-Aug-26 A	0.00	0.00	0.00	100%	100%	14
Crane		207	16-Mar-26	30-Sep-26	16-Feb-26 A	13-Aug-26 A	179,076.09	179,076.09	179,076.09	100%	100%	41
JDH4-02-007-	PO for Crane	7	16-Mar-26	26-Mar-26	16-Feb-26 A	16-Feb-26 A	0.00	0.00	0.00	100%	100%	29
JDH4-02-007-	Material Fabrication for Crane - Stag	19	28-Mar-26	18-Apr-26	17-Feb-26 A	25-Mar-26 A	0.00	0.00	0.00	100%	100%	21
JDH4-02-007-	Material Fabrication for Crane - Stag	20	19-Apr-26	11-May-26	25-Mar-26 A	20-May-26 A	0.00	0.00	0.00	100%	100%	-8
JDH4-02-007-	Material Fabrication for Crane - Stag	30	12-May-26	18-Jun-26	21-May-26 A	03-Aug-26 A	0.00	0.00	0.00	100%	100%	-39
JDH4-02-007-	Material Fabrication for Crane - Stag	30	20-Jun-26	23-Jul-26	01-Aug-26 A	06-Aug-26 A	0.00	0.00	0.00	100%	100%	-12
JDH4-02-007-	Material Delivery for Crane	28	20-Aug-26	21-Sep-26	08-Aug-26 A	12-Aug-26 A	179,076.09	179,076.09	179,076.09	100%	100%	35
JDH4-02-007-	Staging Time for Crane	7	22-Sep-26	30-Sep-26	13-Aug-26 A	13-Aug-26 A	0.00	0.00	0.00	100%	100%	41
Air Vents		254	28-Mar-26	16-Dec-26	25-Feb-26 A	23-May-26 A	0.00	179,076.09	179,076.09	0%	100%	174
JDH4-02-007-	PO for Air Vents	7	28-Mar-26	04-Apr-26	25-Feb-26 A	25-Feb-26 A	0.00	0.00	0.00	100%	100%	29
JDH4-02-007-	Material Fabrication for Air Vents - Sta	14	05-Apr-26	20-Apr-26	26-Feb-26 A	25-Mar-26 A	0.00	0.00	0.00	100%	100%	23
JDH4-02-007-	Material Fabrication for Air Vents - Sta	20	21-Apr-26	13-May-26	25-Mar-26 A	31-Mar-26 A	0.00	0.00	0.00	100%	100%	37
JDH4-02-007-	Material Fabrication for Air Vents - Sta	30	14-May-26	21-Jun-26	01-Apr-26 A	09-Apr-26 A	0.00	0.00	0.00	100%	100%	59
JDH4-02-007-	Material Fabrication for Air Vents - Sta	30	23-Jul-26	26-Aug-26	08-Apr-26 A	16-Apr-26 A	0.00	0.00	0.00	100%	100%	110
JDH4-02-007-	Material Fabrication for Air Vents - Sta	30	27-Aug-26	01-Oct-26	18-Apr-26 A	23-Apr-26 A	0.00	0.00	0.00	100%	100%	134
JDH4-02-007-	Material Fabrication for Air Vents - Sta	30	03-Oct-26	05-Nov-26	25-Apr-26 A	13-May-26 A	0.00	0.00	0.00	53.33%	100%	147
JDH4-02-007-	Material Delivery for Air Vents	28	07-Nov-26	08-Dec-26	14-May-26 A	18-May-26 A	0.00	179,076.09	179,076.09	0%	100%	171
JDH4-02-007-	Staging Time for Air Vents	7	09-Dec-26	16-Dec-26	19-May-26 A	23-May-26 A	0.00	0.00	0.00	0%	100%	174
Screening Container		195	24-Mar-26	15-Nov-26	02-Mar-26 A	02-May-26 A	102,329.19	179,076.09	179,076.09	57.14%	100%	165
JDH4-02-007-	PO for Screening Container	7	24-Mar-26	31-Mar-26	02-Mar-26 A	09-Mar-26 A	0.00	0.00	0.00	100%	100%	16

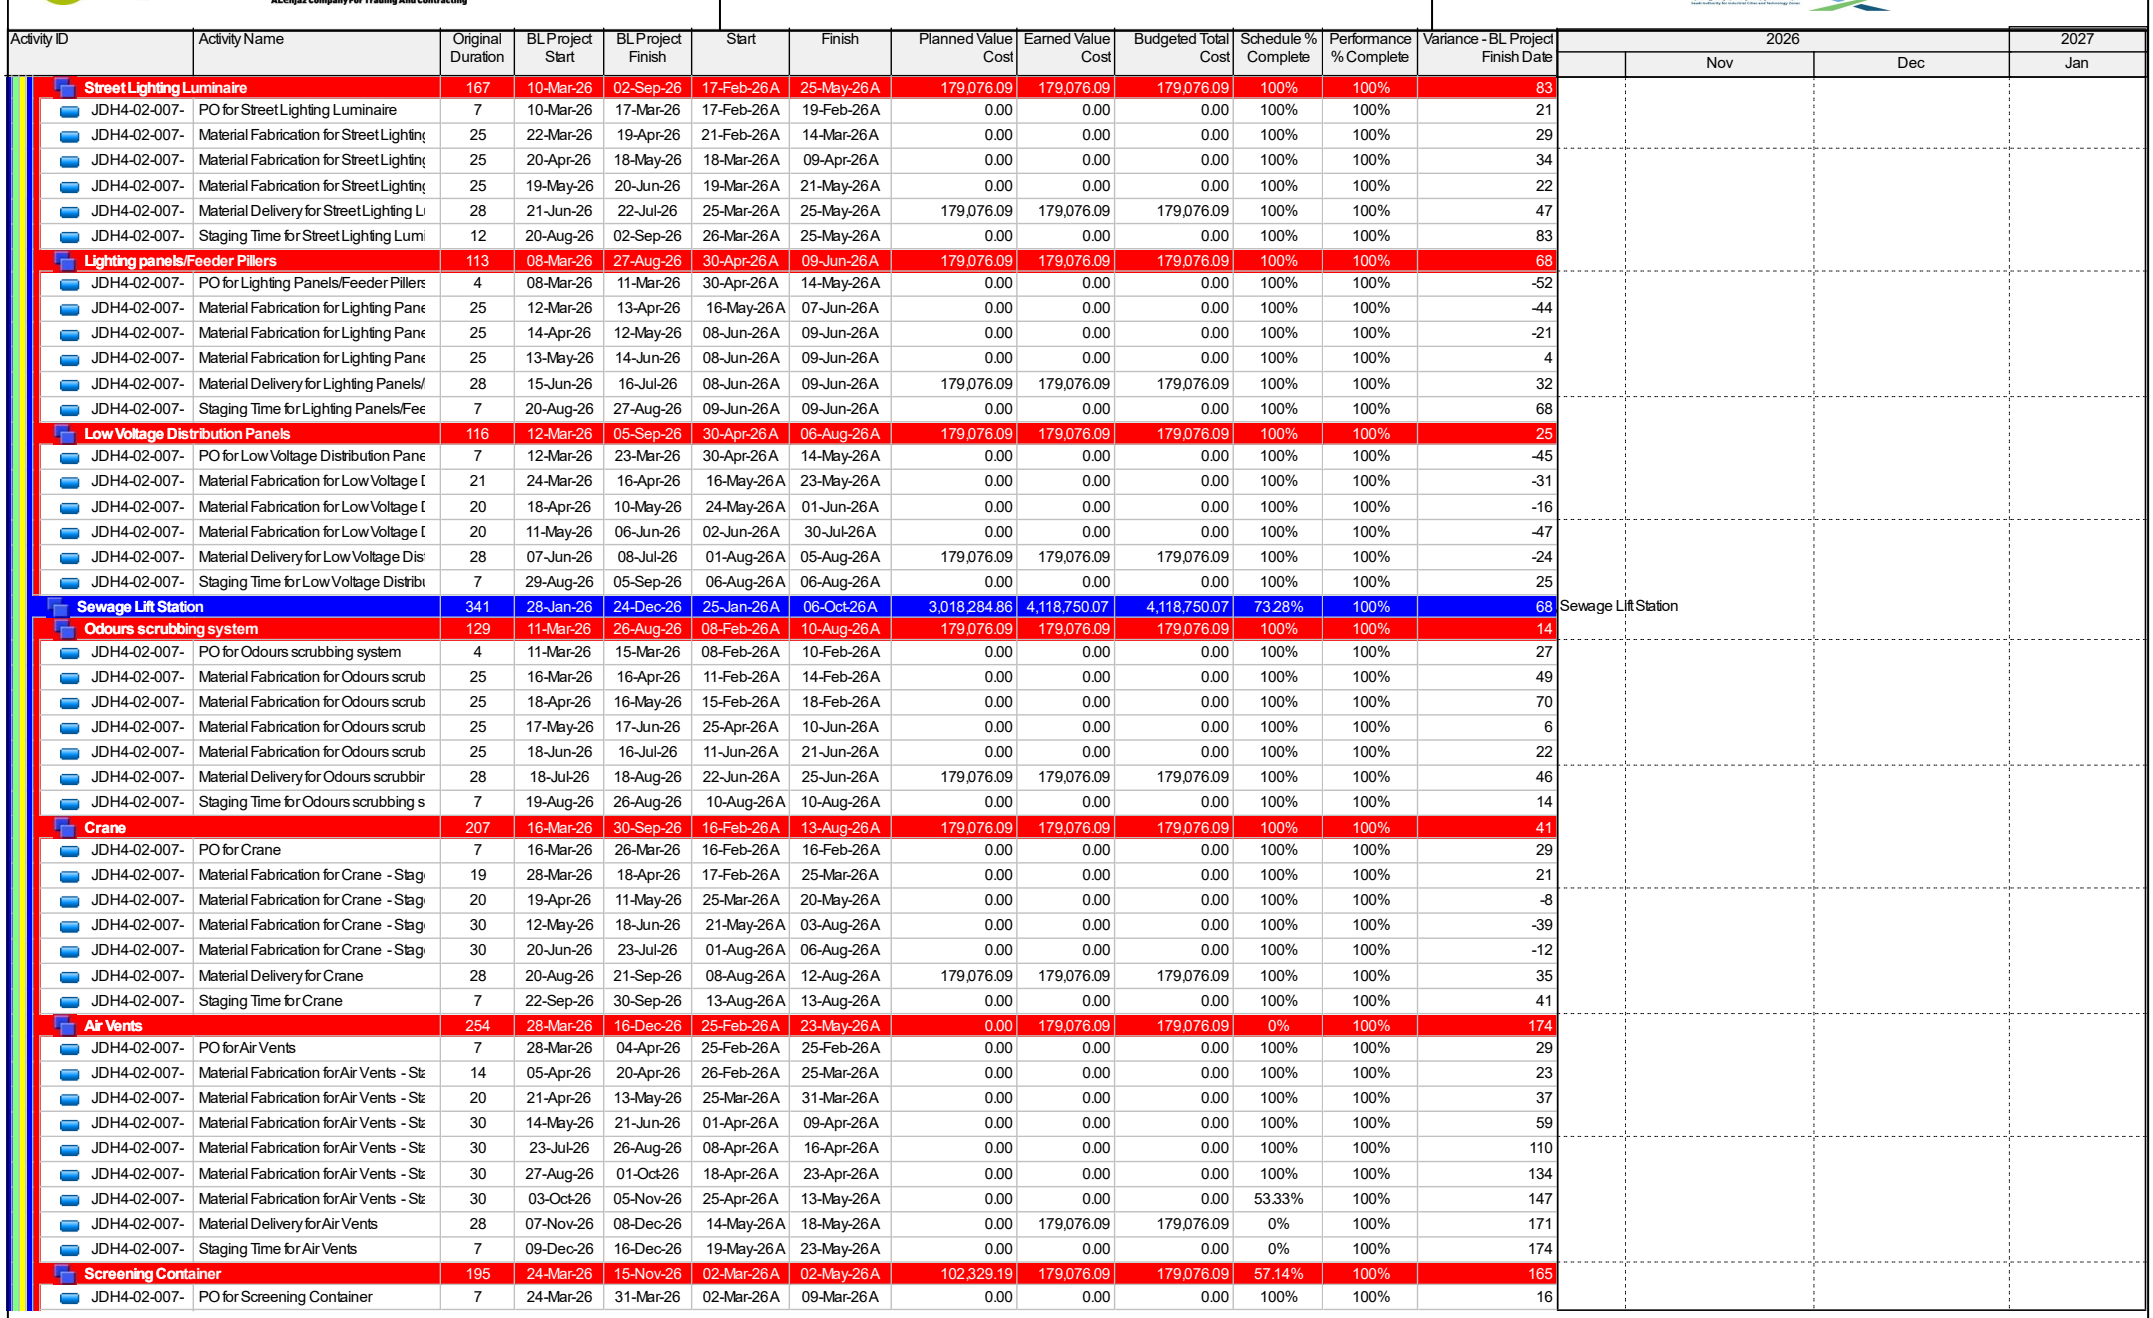

Date	Revision	Checked	Approved


Activity ID	Activity Name	Original Duration	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Schedule % Complete	Performance % Complete	Variance - BL Project Finish Date
JDH4-02-007-	Material Fabrication for Screening Cc	14	01-Apr-26	16-Apr-26	10-Mar-26 A	25-Mar-26 A	0.00	0.00	0.00	100%	100%	20
JDH4-02-007-	Material Fabrication for Screening Cc	20	18-Apr-26	10-May-26	25-Mar-26 A	14-Apr-26 A	0.00	0.00	0.00	100%	100%	22
JDH4-02-007-	Material Fabrication for Screening Cc	30	11-May-26	17-Jun-26	08-Apr-26 A	15-Apr-26 A	0.00	0.00	0.00	100%	100%	51
JDH4-02-007-	Material Fabrication for Screening Cc	30	18-Jun-26	22-Jul-26	16-Apr-26 A	18-Apr-26 A	0.00	0.00	0.00	100%	100%	79
JDH4-02-007-	Material Fabrication for Screening Cc	30	23-Jul-26	26-Aug-26	16-Apr-26 A	18-Apr-26 A	0.00	0.00	0.00	100%	100%	109
JDH4-02-007-	Material Fabrication for Screening Cc	30	27-Aug-26	01-Oct-26	15-Apr-26 A	19-Apr-26 A	0.00	0.00	0.00	100%	100%	138
JDH4-02-007-	Material Delivery for Screening Cont	28	03-Oct-26	03-Nov-26	19-Apr-26 A	23-Apr-26 A	102,329.19	179,076.09	179,076.09	57.14%	100%	162
JDH4-02-007-	Staging Time for Screening Containe	10	04-Nov-26	15-Nov-26	25-Apr-26 A	02-May-26 A	0.00	0.00	0.00	0%	100%	165
Baffle Plates		160	05-Apr-26	29-Sep-26	02-Feb-26 A	24-Feb-26 A	179,076.09	179,076.09	179,076.09	100%	100%	179
JDH4-02-007-	PO for Baffle Plates	7	05-Apr-26	12-Apr-26	02-Feb-26 A	02-Feb-26 A	0.00	0.00	0.00	100%	100%	55
JDH4-02-007-	Material Fabrication for Baffle Plates	30	13-Apr-26	17-May-26	03-Feb-26 A	05-Feb-26 A	0.00	0.00	0.00	100%	100%	82
JDH4-02-007-	Material Fabrication for Baffle Plates	30	18-May-26	24-Jun-26	07-Feb-26 A	08-Feb-26 A	0.00	0.00	0.00	100%	100%	110
JDH4-02-007-	Material Fabrication for Baffle Plates	30	25-Jun-26	29-Jul-26	08-Feb-26 A	09-Feb-26 A	0.00	0.00	0.00	100%	100%	139
JDH4-02-007-	Material Fabrication for Baffle Plates	30	30-Jul-26	02-Sep-26	10-Feb-26 A	10-Feb-26 A	0.00	0.00	0.00	100%	100%	168
JDH4-02-007-	Material Delivery for Baffle Plates	15	03-Sep-26	20-Sep-26	11-Feb-26 A	11-Feb-26 A	179,076.09	179,076.09	179,076.09	100%	100%	182
JDH4-02-007-	Staging Time for Baffle Plates	7	21-Sep-26	29-Sep-26	16-Feb-26 A	24-Feb-26 A	0.00	0.00	0.00	100%	100%	179
Anti-Water Hammer Equipment		206	30-Mar-26	29-Nov-26	02-Feb-26 A	09-Feb-26 A	0.00	179,076.09	179,076.09	0%	100%	243
JDH4-02-007-	PO for Anti-Water Hammer Equipme	8	30-Mar-26	07-Apr-26	02-Feb-26 A	02-Feb-26 A	0.00	0.00	0.00	100%	100%	51
JDH4-02-007-	Material Fabrication for Anti-Water Ha	14	08-Apr-26	23-Apr-26	03-Feb-26 A	03-Feb-26 A	0.00	0.00	0.00	100%	100%	64
JDH4-02-007-	Material Fabrication for Anti-Water Ha	20	25-Apr-26	17-May-26	03-Feb-26 A	03-Feb-26 A	0.00	0.00	0.00	100%	100%	84
JDH4-02-007-	Material Fabrication for Anti-Water Ha	30	18-May-26	24-Jun-26	03-Feb-26 A	04-Feb-26 A	0.00	0.00	0.00	100%	100%	113
JDH4-02-007-	Material Fabrication for Anti-Water Ha	30	25-Jun-26	29-Jul-26	04-Feb-26 A	04-Feb-26 A	0.00	0.00	0.00	100%	100%	143
JDH4-02-007-	Material Fabrication for Anti-Water Ha	30	30-Jul-26	02-Sep-26	04-Feb-26 A	05-Feb-26 A	0.00	0.00	0.00	100%	100%	172
JDH4-02-007-	Material Fabrication for Anti-Water Ha	30	30-Sep-26	03-Nov-26	04-Feb-26 A	05-Feb-26 A	0.00	0.00	0.00	60%	100%	224
JDH4-02-007-	Material Delivery for Anti-Water Ham	15	04-Nov-26	21-Nov-26	03-Feb-26 A	08-Feb-26 A	0.00	179,076.09	179,076.09	0%	100%	237
JDH4-02-007-	Staging Time for Anti-Water Hammer	7	22-Nov-26	29-Nov-26	08-Feb-26 A	09-Feb-26 A	0.00	0.00	0.00	0%	100%	243
Pumps		252	28-Jan-26	14-Sep-26	28-Jan-26 A	05-Oct-26 A	179,076.09	179,076.09	179,076.09	100%	100%	-17
JDH4-02-007-	PO for Pumps	2	28-Jan-26	29-Jan-26	28-Jan-26 A	29-Jan-26 A	0.00	0.00	0.00	100%	100%	0
JDH4-02-007-	Material Fabrication for Pumps - Stag	30	03-Feb-26	10-Mar-26	01-Feb-26 A	14-Feb-26 A	0.00	0.00	0.00	100%	100%	20
JDH4-02-007-	Material Fabrication for Pumps - Stag	30	11-Mar-26	18-Apr-26	16-Feb-26 A	28-Feb-26 A	0.00	0.00	0.00	100%	100%	39
JDH4-02-007-	Material Fabrication for Pumps - Stag	30	19-Apr-26	23-May-26	01-Mar-26 A	20-May-26 A	0.00	0.00	0.00	100%	100%	2
JDH4-02-007-	Material Fabrication for Pumps - Stag	30	24-May-26	30-Jun-26	21-May-26 A	28-Sep-26 A	0.00	0.00	0.00	100%	100%	-76
JDH4-02-007-	Material Fabrication for Pumps - Stag	30	01-Jul-26	04-Aug-26	03-Aug-26 A	27-Sep-26 A	0.00	0.00	0.00	100%	100%	-45
JDH4-02-007-	Material Delivery for Pumps	28	05-Aug-26	06-Sep-26	27-Sep-26 A	30-Sep-26 A	179,076.09	179,076.09	179,076.09	100%	100%	-20
JDH4-02-007-	Staging Time for Pumps	7	07-Sep-26	14-Sep-26	01-Oct-26 A	05-Oct-26 A	0.00	0.00	0.00	100%	100%	-17
Main Distribution Board /MCC panels		113	05-Mar-26	20-Aug-26	07-Jun-26 A	27-Aug-26 A	179,076.09	179,076.09	179,076.09	100%	100%	-6
JDH4-02-007-	PO for Main Distribution Board / MCC	4	05-Mar-26	09-Mar-26	07-Jun-26 A	08-Jun-26 A	0.00	0.00	0.00	100%	100%	-72
JDH4-02-007-	Material Fabrication for Main Distribut	25	10-Mar-26	11-Apr-26	09-Jun-26 A	11-Jun-26 A	0.00	0.00	0.00	100%	100%	-50
JDH4-02-007-	Material Fabrication for Main Distribut	25	12-Apr-26	10-May-26	13-Jun-26 A	15-Jun-26 A	0.00	0.00	0.00	100%	100%	-28
JDH4-02-007-	Material Fabrication for Main Distribut	25	11-May-26	11-Jun-26	01-Aug-26 A	11-Aug-26 A	0.00	0.00	0.00	100%	100%	-51
JDH4-02-007-	Material Fabrication for Main Distribut	25	13-Jun-26	11-Jul-26	01-Aug-26 A	06-Aug-26 A	0.00	0.00	0.00	100%	100%	-23
JDH4-02-007-	Material Delivery for Main Distribution	28	12-Jul-26	12-Aug-26	12-Aug-26 A	19-Aug-26 A	179,076.09	179,076.09	179,076.09	100%	100%	-6
JDH4-02-007-	Staging Time for Main Distribution Bo	7	13-Aug-26	20-Aug-26	20-Aug-26 A	27-Aug-26 A	0.00	0.00	0.00	100%	100%	-6
Final Panel boards		115	01-Mar-26	18-Aug-26	08-Jun-26 A	03-Sep-26 A	179,076.09	179,076.09	179,076.09	100%	100%	-14
JDH4-02-007-	PO for Final Panel Boards	7	01-Mar-26	08-Mar-26	08-Jun-26 A	08-Jun-26 A	0.00	0.00	0.00	100%	100%	-73
JDH4-02-007-	Material Fabrication for Final Panel B	9	09-Mar-26	22-Mar-26	09-Jun-26 A	11-Jun-26 A	0.00	0.00	0.00	100%	100%	-67
JDH4-02-007-	Material Fabrication for Final Panel B	30	23-Mar-26	26-Apr-26	13-Jun-26 A	15-Jun-26 A	0.00	0.00	0.00	100%	100%	-40
JDH4-02-007-	Material Fabrication for Final Panel B	30	27-Apr-26	03-Jun-26	01-Aug-26 A	25-Aug-26 A	0.00	0.00	0.00	100%	100%	-71
JDH4-02-007-	Material Fabrication for Final Panel B	30	04-Jun-26	08-Jul-26	01-Aug-26 A	20-Aug-26 A	0.00	0.00	0.00	100%	100%	-37
JDH4-02-007-	Material Delivery for Final Panel Boa	28	09-Jul-26	10-Aug-26	26-Aug-26 A	27-Aug-26 A	179,076.09	179,076.09	179,076.09	100%	100%	-15

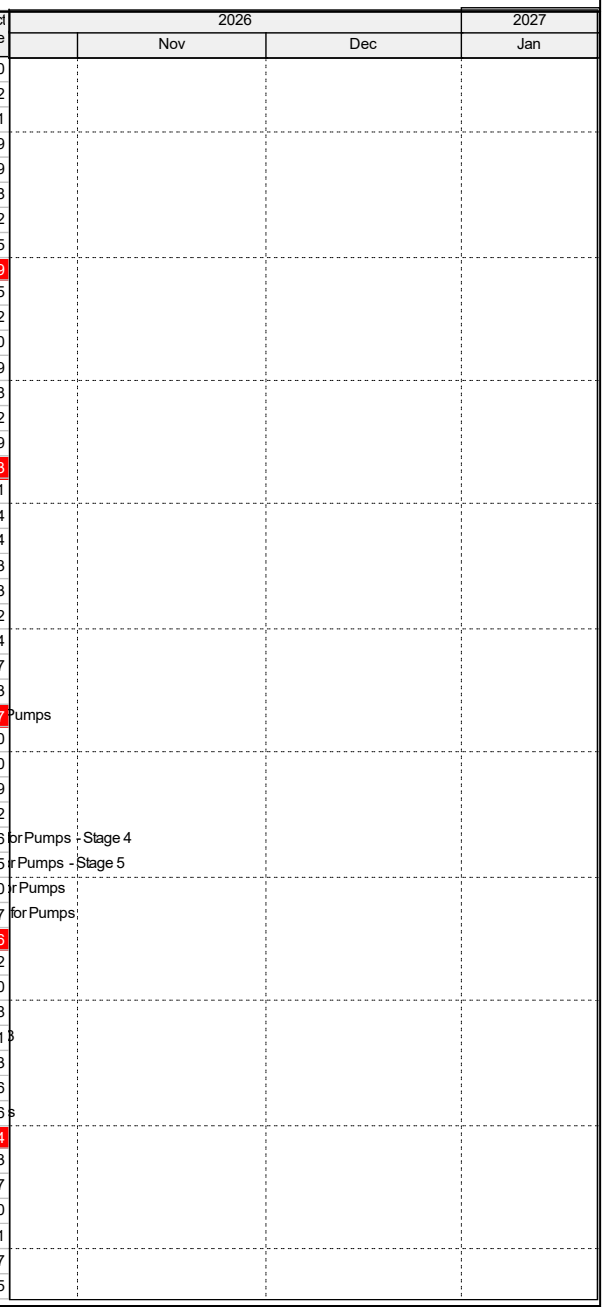

Actual Work
Remaining Work
Critical Remaining Work
Milestone

Date	Revision	Checked	Approved

Activity ID	Activity Name	Original Duration	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Schedule % Complete	Performance % Complete	Variance - BL Project Finish Date
JDH4-02-007-	Staging Time for Final Panel Boards	7	11-Aug-26	18-Aug-26	29-Aug-26 A	03-Sep-26 A	0.00	0.00	0.00	100%	100%	-14
Local Control Panel/ Monitoring Control Panel		154	09-Mar-26	10-Nov-26	26-Jan-26 A	03-Sep-26 A	108,724.77	179,076.09	179,076.09	60.71%	100%	58
JDH4-02-007-	PO for Local Control Panel/ Monitorir	7	09-Mar-26	16-Mar-26	26-Jan-26 A	29-Jan-26 A	0.00	0.00	0.00	100%	100%	38
JDH4-02-007-	Material Fabrication for Local Control	30	17-Mar-26	23-Apr-26	31-Jan-26 A	05-Feb-26 A	0.00	0.00	0.00	100%	100%	62
JDH4-02-007-	Material Fabrication for Local Control	30	25-Apr-26	01-Jun-26	07-Feb-26 A	21-Mar-26 A	0.00	0.00	0.00	100%	100%	59
JDH4-02-007-	Material Fabrication for Local Control	30	02-Jun-26	06-Jul-26	21-Mar-26 A	01-Aug-26 A	0.00	0.00	0.00	100%	100%	-22
JDH4-02-007-	Material Fabrication for Local Control	30	07-Jul-26	10-Aug-26	15-Jul-26 A	19-Aug-26 A	0.00	0.00	0.00	100%	100%	-8
JDH4-02-007-	Material Fabrication for Local Control	30	11-Aug-26	14-Sep-26	15-Jul-26 A	05-Aug-26 A	0.00	0.00	0.00	100%	100%	34
JDH4-02-007-	Material Delivery for Local Control Pa	28	01-Oct-26	02-Nov-26	20-Aug-26 A	27-Aug-26 A	108,724.77	179,076.09	179,076.09	60.71%	100%	57
JDH4-02-007-	Staging Time for Local Control Panel	7	03-Nov-26	10-Nov-26	29-Aug-26 A	03-Sep-26 A	0.00	0.00	0.00	0%	100%	58
Engine Generators		170	28-Mar-26	18-Nov-26	11-May-26 A	28-Jun-26 A	108,724.77	179,076.09	179,076.09	60.71%	100%	122
JDH4-02-007-	PO for Engine Generators	7	28-Mar-26	04-Apr-26	11-May-26 A	11-May-26 A	0.00	0.00	0.00	100%	100%	-32
JDH4-02-007-	Material Fabrication for Engine Gene	30	05-Apr-26	09-May-26	11-May-26 A	11-May-26 A	0.00	0.00	0.00	100%	100%	-2
JDH4-02-007-	Material Fabrication for Engine Gene	30	10-May-26	16-Jun-26	14-May-26 A	16-May-26 A	0.00	0.00	0.00	100%	100%	24
JDH4-02-007-	Material Fabrication for Engine Gene	30	17-Jun-26	21-Jul-26	17-May-26 A	27-May-26 A	0.00	0.00	0.00	100%	100%	46
JDH4-02-007-	Material Fabrication for Engine Gene	30	22-Jul-26	25-Aug-26	28-May-26 A	06-Jun-26 A	0.00	0.00	0.00	100%	100%	69
JDH4-02-007-	Material Fabrication for Engine Gene	30	26-Aug-26	30-Sep-26	08-Jun-26 A	20-Jun-26 A	0.00	0.00	0.00	100%	100%	87
JDH4-02-007-	Material Delivery for Engine Generat	28	01-Oct-26	02-Nov-26	21-Jun-26 A	27-Jun-26 A	108,724.77	179,076.09	179,076.09	60.71%	100%	109
JDH4-02-007-	Staging Time for Engine Generators	7	11-Nov-26	18-Nov-26	28-Jun-26 A	28-Jun-26 A	0.00	0.00	0.00	0%	100%	122
Standby Diesel Generator		141	16-Mar-26	07-Oct-26	11-May-26 A	29-Jun-26 A	179,076.09	179,076.09	179,076.09	100%	100%	85
JDH4-02-007-	PO for Standby Diesel Generator	7	16-Mar-26	26-Mar-26	11-May-26 A	11-May-26 A	0.00	0.00	0.00	100%	100%	-39
JDH4-02-007-	Material Fabrication for Standby Dies	30	28-Mar-26	30-Apr-26	12-May-26 A	16-May-26 A	0.00	0.00	0.00	100%	100%	-13
JDH4-02-007-	Material Fabrication for Standby Dies	30	02-May-26	08-Jun-26	17-May-26 A	31-May-26 A	0.00	0.00	0.00	100%	100%	7
JDH4-02-007-	Material Fabrication for Standby Dies	30	09-Jun-26	13-Jul-26	01-Jun-26 A	13-Jun-26 A	0.00	0.00	0.00	100%	100%	27
JDH4-02-007-	Material Fabrication for Standby Dies	30	14-Jul-26	17-Aug-26	14-Jun-26 A	23-Jun-26 A	0.00	0.00	0.00	100%	100%	48
JDH4-02-007-	Material Delivery for Standby Diesel (	14	18-Aug-26	02-Sep-26	24-Jun-26 A	27-Jun-26 A	179,076.09	179,076.09	179,076.09	100%	100%	59
JDH4-02-007-	Staging Time for Standby Diesel Ger	7	30-Sep-26	07-Oct-26	28-Jun-26 A	29-Jun-26 A	0.00	0.00	0.00	100%	100%	85
Power Factor Correction Capacitor Bank		165	01-Mar-26	24-Dec-26	26-Jan-26 A	30-Aug-26 A	70,351.32	179,076.09	179,076.09	39.29%	100%	99
JDH4-02-007-	PO for Power Factor Correction Capa	16	01-Mar-26	22-Mar-26	26-Jan-26 A	29-Jan-26 A	0.00	0.00	0.00	100%	100%	40
JDH4-02-007-	Material Fabrication for Power Factor	14	23-Mar-26	07-Apr-26	31-Jan-26 A	28-Feb-26 A	0.00	0.00	0.00	100%	100%	30
JDH4-02-007-	Material Fabrication for Power Factor	20	08-Apr-26	30-Apr-26	01-Mar-26 A	28-Mar-26 A	0.00	0.00	0.00	100%	100%	29
JDH4-02-007-	Material Fabrication for Power Factor	30	02-May-26	08-Jun-26	30-Mar-26 A	25-Apr-26 A	0.00	0.00	0.00	100%	100%	35
JDH4-02-007-	Material Fabrication for Power Factor	30	09-Jun-26	13-Jul-26	26-Apr-26 A	06-Aug-26 A	0.00	0.00	0.00	100%	100%	-21
JDH4-02-007-	Material Fabrication for Power Factor	30	14-Jul-26	17-Aug-26	11-Jul-26 A	15-Aug-26 A	0.00	0.00	0.00	100%	100%	2
JDH4-02-007-	Material Fabrication for Power Factor	30	18-Aug-26	21-Sep-26	11-Jul-26 A	08-Aug-26 A	0.00	0.00	0.00	100%	100%	38
JDH4-02-007-	Material Delivery for Power Factor Cc	28	08-Oct-26	09-Nov-26	16-Aug-26 A	26-Aug-26 A	70,351.32	179,076.09	179,076.09	39.29%	100%	63
JDH4-02-007-	Staging Time for Power Factor Corre	7	17-Dec-26	24-Dec-26	27-Aug-26 A	30-Aug-26 A	0.00	0.00	0.00	0%	100%	99
Low-Voltage Electrical Power Conductors and Cable		141	16-Mar-26	31-Aug-26	25-Feb-26 A	25-Jul-26 A	179,076.09	179,076.09	179,076.09	100%	100%	32
JDH4-02-007-	PO for Low-Voltage Electrical Power	4	16-Mar-26	23-Mar-26	25-Feb-26 A	25-Feb-26 A	0.00	0.00	0.00	100%	100%	19
JDH4-02-007-	Material Fabrication for Low-Voltage	25	24-Mar-26	21-Apr-26	26-Feb-26 A	05-Mar-26 A	0.00	0.00	0.00	100%	100%	37
JDH4-02-007-	Material Fabrication for Low-Voltage	25	22-Apr-26	20-May-26	07-Mar-26 A	11-Mar-26 A	0.00	0.00	0.00	100%	100%	57
JDH4-02-007-	Material Fabrication for Low-Voltage	25	21-May-26	22-Jun-26	12-Mar-26 A	19-Mar-26 A	0.00	0.00	0.00	100%	100%	77
JDH4-02-007-	Material Fabrication for Low-Voltage	25	23-Jun-26	21-Jul-26	22-Mar-26 A	16-Jul-26 A	0.00	0.00	0.00	100%	100%	4
JDH4-02-007-	Material Delivery for Low-Voltage Ele	28	22-Jul-26	23-Aug-26	15-Apr-26 A	23-Jul-26 A	179,076.09	179,076.09	179,076.09	100%	100%	26
JDH4-02-007-	Staging Time for Low-Voltage Electri	7	24-Aug-26	31-Aug-26	16-Apr-26 A	25-Jul-26 A	0.00	0.00	0.00	100%	100%	32
Low Voltage Feeder Cable		106	24-Mar-26	07-Sep-26	25-Feb-26 A	10-May-26 A	179,076.09	179,076.09	179,076.09	100%	100%	100
JDH4-02-007-	PO for Low Voltage Feeder Cable	7	24-Mar-26	31-Mar-26	25-Feb-26 A	25-Feb-26 A	0.00	0.00	0.00	100%	100%	26
JDH4-02-007-	Material Fabrication for Low Voltage F	9	01-Apr-26	11-Apr-26	26-Feb-26 A	05-Mar-26 A	0.00	0.00	0.00	100%	100%	28
JDH4-02-007-	Material Fabrication for Low Voltage F	30	12-Apr-26	16-May-26	07-Mar-26 A	12-Mar-26 A	0.00	0.00	0.00	100%	100%	52
JDH4-02-007-	Material Fabrication for Low Voltage F	30	17-May-26	23-Jun-26	14-Mar-26 A	28-Mar-26 A	0.00	0.00	0.00	100%	100%	72

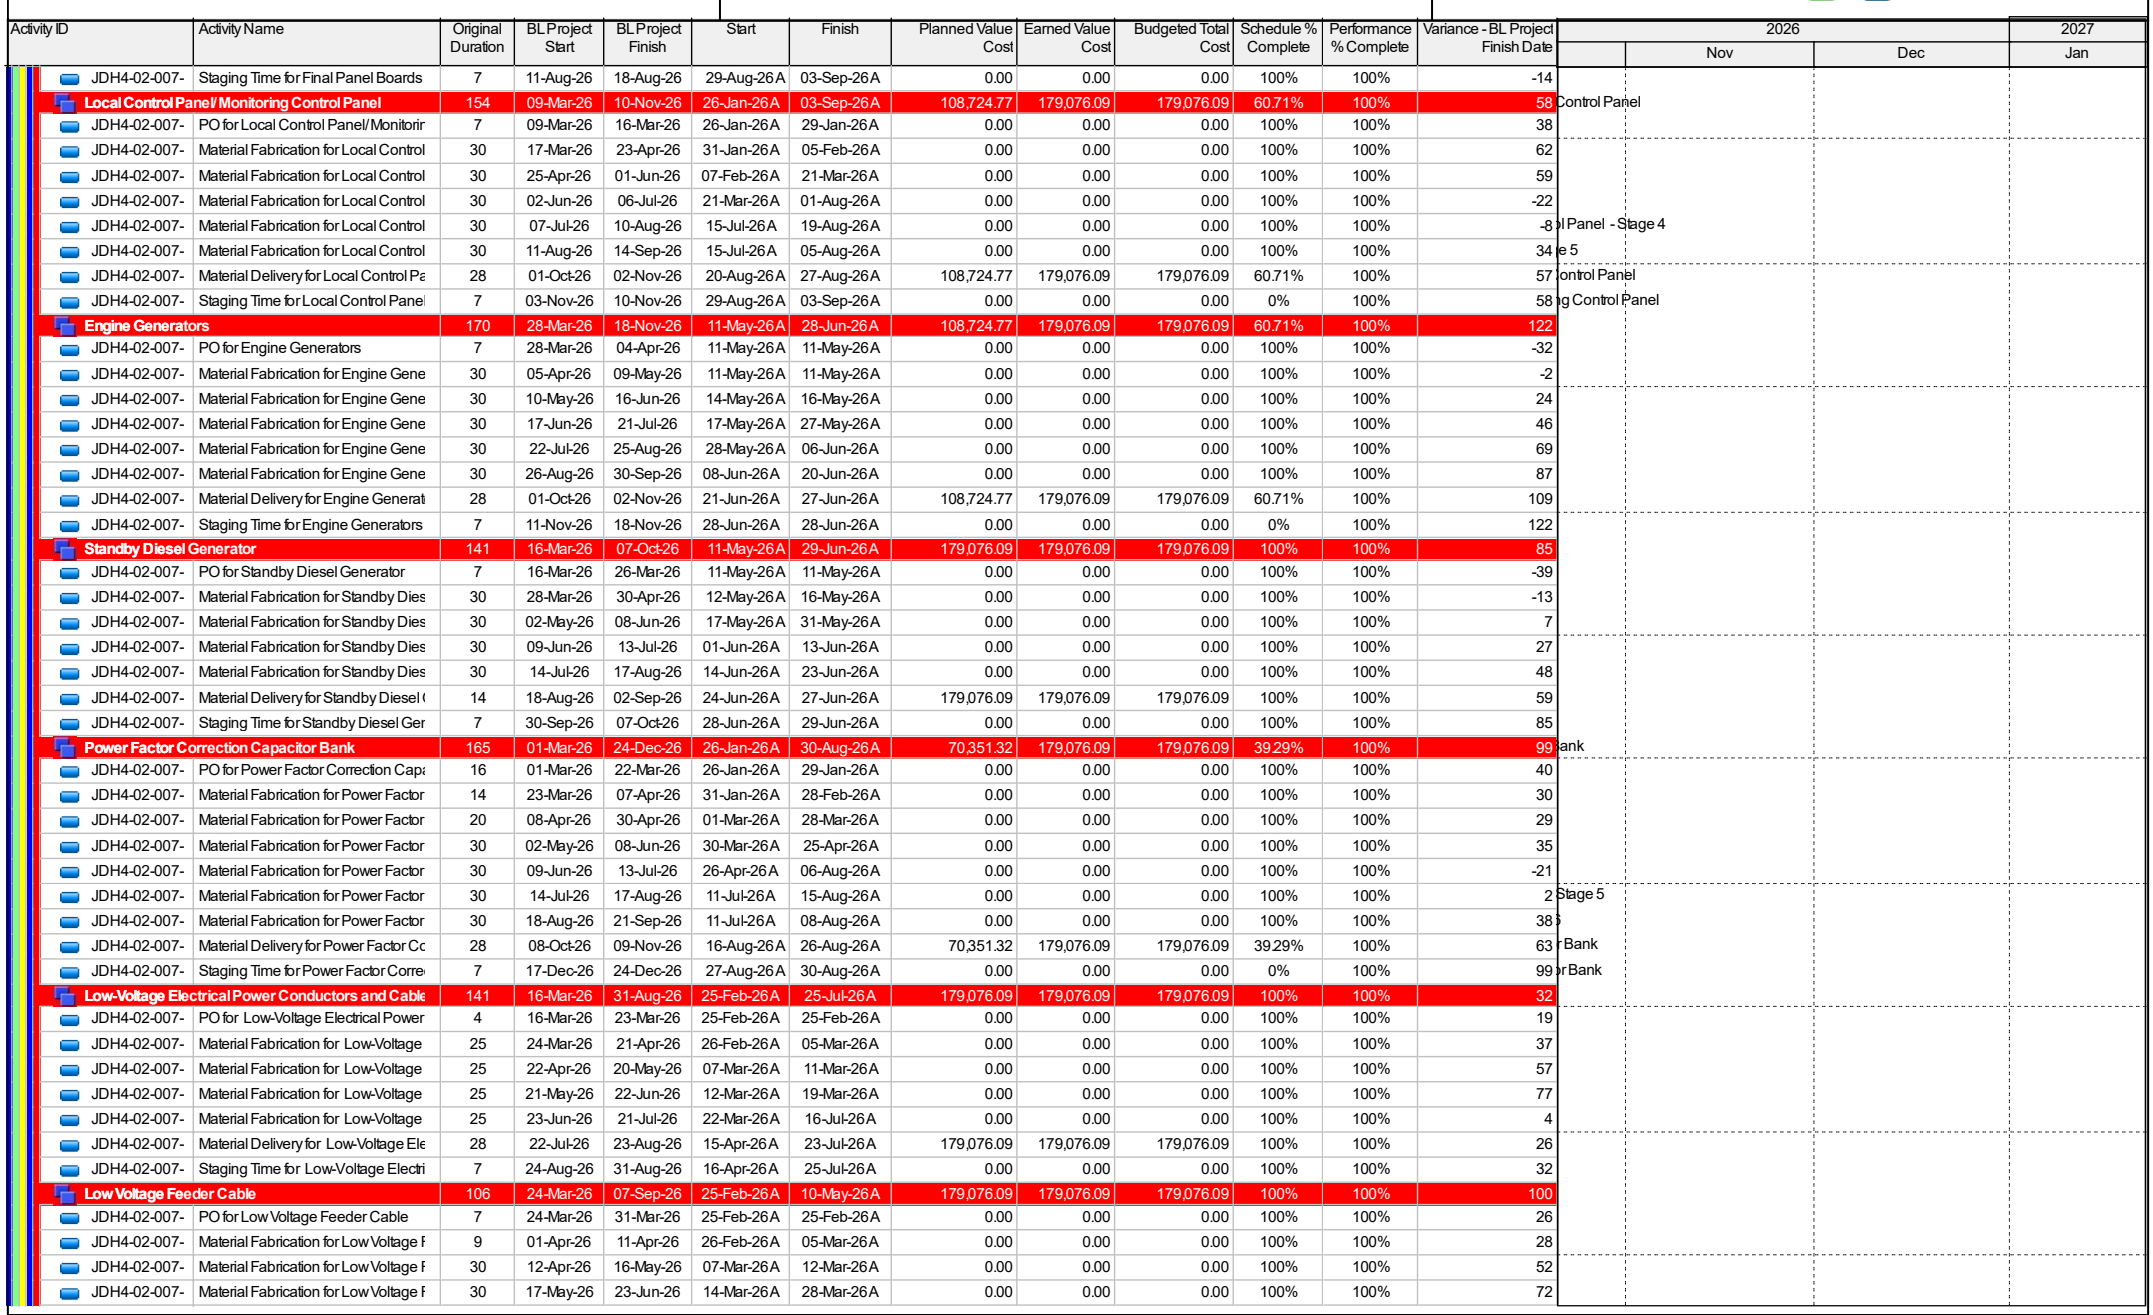


Date	Revision	Checked	Approved

Activity ID	Activity Name	Original Duration	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Schedule % Complete	Performance % Complete	Variance - BL Project Finish Date
JDH4-02-007-	Material Fabrication for Low Voltage F	30	24-Jun-26	28-Jul-26	30-Mar-26 A	05-May-26 A	0.00	0.00	0.00	100%	100%	69
JDH4-02-007-	Material Delivery for Low Voltage Fee	28	29-Jul-26	30-Aug-26	07-May-26 A	07-May-26 A	179,076.09	179,076.09	179,076.09	100%	100%	95
JDH4-02-007-	Staging Time for Low Voltage Feede	7	31-Aug-26	07-Sep-26	09-May-26 A	10-May-26 A	0.00	0.00	0.00	100%	100%	100
Wiring Devices		243	02-Mar-26	26-Nov-26	23-Feb-26 A	06-May-26 A	131,322.47	179,076.09	179,076.09	73.33%	100%	171
JDH4-02-007-	PO for Wiring Devices	7	02-Mar-26	09-Mar-26	23-Feb-26 A	26-Mar-26 A	0.00	0.00	0.00	100%	100%	-12
JDH4-02-007-	Material Fabrication for Wiring Devic	14	10-Mar-26	29-Mar-26	26-Feb-26 A	28-Feb-26 A	0.00	0.00	0.00	100%	100%	22
JDH4-02-007-	Material Fabrication for Wiring Devic	20	30-Mar-26	21-Apr-26	28-Feb-26 A	03-Mar-26 A	0.00	0.00	0.00	100%	100%	39
JDH4-02-007-	Material Fabrication for Wiring Devic	30	22-Apr-26	30-May-26	04-Mar-26 A	07-Mar-26 A	0.00	0.00	0.00	100%	100%	66
JDH4-02-007-	Material Fabrication for Wiring Devic	30	31-May-26	04-Jul-26	08-Mar-26 A	14-Mar-26 A	0.00	0.00	0.00	100%	100%	90
JDH4-02-007-	Material Fabrication for Wiring Devic	30	05-Jul-26	08-Aug-26	15-Mar-26 A	23-Mar-26 A	0.00	0.00	0.00	100%	100%	115
JDH4-02-007-	Material Fabrication for Wiring Devic	30	09-Aug-26	12-Sep-26	26-Mar-26 A	30-Mar-26 A	0.00	0.00	0.00	100%	100%	139
JDH4-02-007-	Material Delivery for Wiring Devices	15	08-Oct-26	25-Oct-26	02-Apr-26 A	06-Apr-26 A	131,322.47	179,076.09	179,076.09	73.33%	100%	169
JDH4-02-007-	Staging Time for Wiring Devices	7	19-Nov-26	26-Nov-26	06-May-26 A	06-May-26 A	0.00	0.00	0.00	0%	100%	171
Enclosed Switches and Circuit Breakers		174	01-Apr-26	19-Nov-26	17-Mar-26 A	26-Aug-26 A	57,560.17	179,076.09	179,076.09	32.14%	100%	72
JDH4-02-007-	PO for Enclosed Switches and Circui	7	01-Apr-26	08-Apr-26	17-Mar-26 A	17-Mar-26 A	0.00	0.00	0.00	100%	100%	16
JDH4-02-007-	Material Fabrication for Enclosed Swi	14	09-Apr-26	25-Apr-26	18-Mar-26 A	29-Mar-26 A	0.00	0.00	0.00	100%	100%	23
JDH4-02-007-	Material Fabrication for Enclosed Swi	20	26-Apr-26	18-May-26	30-Mar-26 A	06-Apr-26 A	0.00	0.00	0.00	100%	100%	36
JDH4-02-007-	Material Fabrication for Enclosed Swi	30	19-May-26	25-Jun-26	07-Apr-26 A	13-Jun-26 A	0.00	0.00	0.00	100%	100%	12
JDH4-02-007-	Material Fabrication for Enclosed Swi	30	27-Jun-26	30-Jul-26	01-Aug-26 A	16-Aug-26 A	0.00	0.00	0.00	100%	100%	-14 Stage 4
JDH4-02-007-	Material Fabrication for Enclosed Swi	30	01-Aug-26	03-Sep-26	01-Aug-26 A	13-Aug-26 A	0.00	0.00	0.00	100%	100%	18 age 5
JDH4-02-007-	Material Fabrication for Enclosed Swi	30	05-Sep-26	10-Oct-26	01-Aug-26 A	05-Aug-26 A	0.00	0.00	0.00	100%	100%	55
JDH4-02-007-	Material Delivery for Enclosed Switch	28	11-Oct-26	11-Nov-26	17-Aug-26 A	23-Aug-26 A	57,560.17	179,076.09	179,076.09	32.14%	100%	68 ers
JDH4-02-007-	Staging Time for Enclosed Switches	7	12-Nov-26	19-Nov-26	23-Aug-26 A	26-Aug-26 A	0.00	0.00	0.00	0%	100%	72 ers
Raceways for Electrical Systems		162	03-Mar-26	15-Sep-26	21-Feb-26 A	09-Apr-26 A	179,076.09	179,076.09	179,076.09	100%	100%	133
JDH4-02-007-	PO for Raceways for Electrical Syster	7	03-Mar-26	10-Mar-26	21-Feb-26 A	21-Feb-26 A	0.00	0.00	0.00	100%	100%	14
JDH4-02-007-	Material Fabrication for Raceways for	30	11-Mar-26	18-Apr-26	22-Feb-26 A	23-Feb-26 A	0.00	0.00	0.00	100%	100%	43
JDH4-02-007-	Material Fabrication for Raceways for	30	19-Apr-26	23-May-26	24-Feb-26 A	28-Feb-26 A	0.00	0.00	0.00	100%	100%	69
JDH4-02-007-	Material Fabrication for Raceways for	30	24-May-26	30-Jun-26	01-Mar-26 A	10-Mar-26 A	0.00	0.00	0.00	100%	100%	90
JDH4-02-007-	Material Fabrication for Raceways for	30	01-Jul-26	04-Aug-26	11-Mar-26 A	14-Mar-26 A	0.00	0.00	0.00	100%	100%	117
JDH4-02-007-	Material Delivery for Raceways for El	28	05-Aug-26	06-Sep-26	14-Mar-26 A	19-Mar-26 A	179,076.09	179,076.09	179,076.09	100%	100%	142
JDH4-02-007-	Staging Time for Raceways for Electr	7	08-Sep-26	15-Sep-26	01-Apr-26 A	09-Apr-26 A	0.00	0.00	0.00	100%	100%	133
Electrical Manholes		312	25-Feb-26	24-Dec-26	10-Feb-26 A	26-Apr-26 A	143,260.87	179,076.09	179,076.09	80%	100%	204
JDH4-02-007-	PO for Electrical Manholes	16	25-Feb-26	15-Mar-26	10-Feb-26 A	12-Feb-26 A	0.00	0.00	0.00	100%	100%	25
JDH4-02-007-	Material Fabrication for Electrical Mar	14	16-Mar-26	04-Apr-26	14-Feb-26 A	08-Apr-26 A	0.00	0.00	0.00	100%	100%	-4
JDH4-02-007-	Material Fabrication for Electrical Mar	20	05-Apr-26	27-Apr-26	08-Apr-26 A	11-Apr-26 A	0.00	0.00	0.00	100%	100%	14
JDH4-02-007-	Material Fabrication for Electrical Mar	30	28-Apr-26	04-Jun-26	08-Apr-26 A	19-Apr-26 A	0.00	0.00	0.00	100%	100%	37
JDH4-02-007-	Material Fabrication for Electrical Mar	30	06-Jun-26	09-Jul-26	12-Apr-26 A	19-Apr-26 A	0.00	0.00	0.00	100%	100%	67
JDH4-02-007-	Material Fabrication for Electrical Mar	30	11-Jul-26	13-Aug-26	13-Apr-26 A	16-Apr-26 A	0.00	0.00	0.00	100%	100%	99
JDH4-02-007-	Material Fabrication for Electrical Mar	30	01-Sep-26	06-Oct-26	16-Apr-26 A	20-Apr-26 A	0.00	0.00	0.00	100%	100%	141
JDH4-02-007-	Material Delivery for Electrical Manho	15	07-Oct-26	24-Oct-26	18-Apr-26 A	22-Apr-26 A	143,260.87	179,076.09	179,076.09	80%	100%	154
JDH4-02-007-	Staging Time for Electrical Manholes	7	17-Dec-26	24-Dec-26	24-Apr-26 A	26-Apr-26 A	0.00	0.00	0.00	0%	100%	204
ICT (Data& telephone System)		215	01-Apr-26	19-Nov-26	21-Mar-26 A	14-Apr-26 A	57,560.17	179,076.09	179,076.09	32.14%	100%	184
JDH4-02-007-	PO for ICT (Data& telephone System	7	01-Apr-26	08-Apr-26	21-Mar-26 A	23-Mar-26 A	0.00	0.00	0.00	100%	100%	14
JDH4-02-007-	Material Fabrication for ICT (Data& te	14	09-Apr-26	25-Apr-26	23-Mar-26 A	25-Mar-26 A	0.00	0.00	0.00	100%	100%	26
JDH4-02-007-	Material Fabrication for ICT (Data& te	20	26-Apr-26	18-May-26	25-Mar-26 A	28-Mar-26 A	0.00	0.00	0.00	100%	100%	44
JDH4-02-007-	Material Fabrication for ICT (Data& te	30	19-May-26	25-Jun-26	29-Mar-26 A	30-Mar-26 A	0.00	0.00	0.00	100%	100%	72
JDH4-02-007-	Material Fabrication for ICT (Data& te	30	27-Jun-26	30-Jul-26	31-Mar-26 A	01-Apr-26 A	0.00	0.00	0.00	100%	100%	100
JDH4-02-007-	Material Fabrication for ICT (Data& te	30	01-Aug-26	03-Sep-26	02-Apr-26 A	06-Apr-26 A	0.00	0.00	0.00	100%	100%	126
JDH4-02-007-	Material Fabrication for ICT (Data& te	30	05-Sep-26	10-Oct-26	07-Apr-26 A	09-Apr-26 A	0.00	0.00	0.00	100%	100%	153
JDH4-02-007-	Material Delivery for ICT (Data& telep	28	11-Oct-26	11-Nov-26	12-Apr-26 A	12-Apr-26 A	57,560.17	179,076.09	179,076.09	32.14%	100%	179

2026		2027
Nov	Dec	Jan


Date	Revision	Checked	Approved

Activity ID	Activity Name	Original Duration	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Schedule % Complete	Performance % Complete	Variance - BL Project Finish Date
JDH4-02-007-	Staging Time for ICT (Data& telephor	7	12-Nov-26	19-Nov-26	12-Apr-26 A	14-Apr-26 A	0.00	0.00	0.00	0%	100%	184
Programmable Logic Controllers		204	09-Mar-26	01-Nov-26	25-Jan-26 A	06-Oct-26 A	166,284.94	179,076.09	179,076.09	92.86%	100%	22
JDH4-02-007-	PO for Programmable Logic Controll	7	09-Mar-26	16-Mar-26	25-Jan-26 A	29-Jan-26 A	0.00	0.00	0.00	100%	100%	38
JDH4-02-007-	Material Fabrication for Programmab	14	17-Mar-26	05-Apr-26	01-Feb-26 A	12-Feb-26 A	0.00	0.00	0.00	100%	100%	40
JDH4-02-007-	Material Fabrication for Programmab	20	06-Apr-26	28-Apr-26	14-Feb-26 A	21-Feb-26 A	0.00	0.00	0.00	100%	100%	53
JDH4-02-007-	Material Fabrication for Programmab	30	29-Apr-26	06-Jun-26	22-Feb-26 A	04-Jun-26 A	0.00	0.00	0.00	100%	100%	1
JDH4-02-007-	Material Fabrication for Programmab	30	07-Jun-26	11-Jul-26	06-Jun-26 A	29-Sep-26 A	0.00	0.00	0.00	100%	100%	-68
JDH4-02-007-	Material Fabrication for Programmab	30	12-Jul-26	15-Aug-26	06-Jun-26 A	20-Aug-26 A	0.00	0.00	0.00	100%	100%	-5
JDH4-02-007-	Material Fabrication for Programmab	30	16-Aug-26	19-Sep-26	06-Jun-26 A	27-Sep-26 A	0.00	0.00	0.00	100%	100%	-6
JDH4-02-007-	Material Delivery for Programmable I	28	20-Sep-26	22-Oct-26	30-Sep-26 A	04-Oct-26 A	166,284.94	179,076.09	179,076.09	92.86%	100%	16
JDH4-02-007-	Staging Time for Programmable Log	7	25-Oct-26	01-Nov-26	05-Oct-26 A	06-Oct-26 A	0.00	0.00	0.00	0%	100%	22
Process Control Wiring		178	26-Feb-26	24-Sep-26	25-Jan-26 A	04-Oct-26 A	179,076.09	179,076.09	179,076.09	100%	100%	-8
JDH4-02-007-	PO for Process Control Wiring	12	26-Feb-26	11-Mar-26	25-Jan-26 A	29-Jan-26 A	0.00	0.00	0.00	100%	100%	34
JDH4-02-007-	Material Fabrication for Process Con	30	12-Mar-26	19-Apr-26	30-Jan-26 A	07-Feb-26 A	0.00	0.00	0.00	100%	100%	57
JDH4-02-007-	Material Fabrication for Process Con	30	20-Apr-26	24-May-26	09-Feb-26 A	19-Feb-26 A	0.00	0.00	0.00	100%	100%	76
JDH4-02-007-	Material Fabrication for Process Con	30	25-May-26	01-Jul-26	21-Feb-26 A	27-Sep-26 A	0.00	0.00	0.00	100%	100%	-74
JDH4-02-007-	Material Fabrication for Process Con	30	02-Jul-26	05-Aug-26	01-Aug-26 A	28-Sep-26 A	0.00	0.00	0.00	100%	100%	-45
JDH4-02-007-	Material Delivery for Process Control	28	06-Aug-26	07-Sep-26	29-Sep-26 A	29-Sep-26 A	179,076.09	179,076.09	179,076.09	100%	100%	-18
JDH4-02-007-	Staging Time for Process Control Wi	7	16-Sep-26	24-Sep-26	30-Sep-26 A	04-Oct-26 A	0.00	0.00	0.00	100%	100%	-8
Instrumentation for Process Systems		211	10-Mar-26	11-Nov-26	25-Jan-26 A	30-Aug-26 A	102,329.19	179,076.09	179,076.09	57.14%	100%	62
JDH4-02-007-	PO for Instrumentation for Process S	16	10-Mar-26	31-Mar-26	25-Jan-26 A	29-Jan-26 A	0.00	0.00	0.00	100%	100%	48
JDH4-02-007-	Material Fabrication for Instrumentati	14	01-Apr-26	16-Apr-26	01-Feb-26 A	12-Feb-26 A	0.00	0.00	0.00	100%	100%	50
JDH4-02-007-	Material Fabrication for Instrumentati	20	18-Apr-26	10-May-26	14-Feb-26 A	21-Feb-26 A	0.00	0.00	0.00	100%	100%	63
JDH4-02-007-	Material Fabrication for Instrumentati	30	11-May-26	17-Jun-26	22-Feb-26 A	16-Jul-26 A	0.00	0.00	0.00	100%	100%	-25
JDH4-02-007-	Material Fabrication for Instrumentati	30	18-Jun-26	22-Jul-26	01-Aug-26 A	19-Aug-26 A	0.00	0.00	0.00	100%	100%	-24
JDH4-02-007-	Material Fabrication for Instrumentati	30	23-Jul-26	26-Aug-26	01-Aug-26 A	12-Aug-26 A	0.00	0.00	0.00	100%	100%	13
JDH4-02-007-	Material Fabrication for Instrumentati	30	27-Aug-26	01-Oct-26	01-Aug-26 A	05-Aug-26 A	0.00	0.00	0.00	100%	100%	48
JDH4-02-007-	Material Delivery for Instrumentation	28	03-Oct-26	03-Nov-26	22-Aug-26 A	26-Aug-26 A	102,329.19	179,076.09	179,076.09	57.14%	100%	58
JDH4-02-007-	Staging Time for Instrumentation for I	7	04-Nov-26	11-Nov-26	26-Aug-26 A	30-Aug-26 A	0.00	0.00	0.00	0%	100%	62
Construction		453	04-Dec-25	06-May-27	04-Dec-25 A	29-Dec-26	22,490,507.97	37,015,596.91	38,393,913.07	58.58%	96.41%	106
Demolition Works		227	18-Dec-25	07-Jun-26	18-Dec-25 A	04-Oct-26 A	505,616.54	505,616.54	505,616.54	100%	100%	-100
Demolition in Road network		180	03-Feb-26	29-Mar-26	31-Jan-26 A	29-Aug-26 A	127,411.78	127,411.78	127,411.78	100%	100%	-128
JDH4-02-007-C	Concrete demolition works at the exi	5	03-Feb-26	08-Feb-26	31-Jan-26 A	19-Feb-26 A	26,491.56	26,491.56	26,491.56	100%	100%	-10
JDH4-02-007-C	Removal of the existing asphalt layer	16	09-Feb-26	28-Feb-26	16-Apr-26 A	25-Jun-26 A	37,845.08	37,845.08	37,845.08	100%	100%	-95
JDH4-02-007-C	Milling of the existing asphalt layer [D	15	01-Mar-26	17-Mar-26	15-Apr-26 A	24-Jun-26 A	25,230.06	25,230.06	25,230.06	100%	100%	-79
JDH4-02-007-C	Re-use and compaction of the existir	7	22-Mar-26	29-Mar-26	20-Aug-26 A	29-Aug-26 A	37,845.08	37,845.08	37,845.08	100%	100%	-128
Demolition in TSE network		101	18-Dec-25	14-Feb-26	18-Dec-25 A	17-Mar-26 A	92,720.45	92,720.45	92,720.45	100%	100%	-26
JDH4-02-007-C	Pipe with diameter 63 mm pipe [Dem	10	18-Dec-25	29-Dec-25	18-Dec-25 A	29-Dec-25 A	1,892.25	1,892.25	1,892.25	100%	100%	0
JDH4-02-007-C	Pipe with diameter 200 mm pipe [De	10	18-Dec-25	29-Dec-25	18-Dec-25 A	29-Dec-25 A	47,937.11	47,937.11	47,937.11	100%	100%	0
JDH4-02-007-C	Pipe with diameter 250 mm pipe [De	10	03-Feb-26	14-Feb-26	10-Mar-26 A	17-Mar-26 A	18,922.54	18,922.54	18,922.54	100%	100%	-26
JDH4-02-007-C	Wash out valve with chamber; on 20	10	18-Dec-25	29-Dec-25	18-Dec-25 A	29-Dec-25 A	20,184.04	20,184.04	20,184.04	100%	100%	0
JDH4-02-007-C	Gate valves on 200 mm pipeline [De	10	18-Dec-25	29-Dec-25	18-Dec-25 A	29-Dec-25 A	3,784.51	3,784.51	3,784.51	100%	100%	0
Demolition in Storm water network		218	25-Dec-25	15-Mar-26	25-Dec-25 A	26-Aug-26 A	56,073.80	56,073.80	56,073.80	100%	100%	-135
JDH4-02-007-C	Manhole [Demolition Works]	4	25-Dec-25	29-Dec-25	25-Dec-25 A	29-Dec-25 A	8,830.52	8,830.52	8,830.52	100%	100%	0
JDH4-02-007-C	Baffle box with dimentions 3.04x7.80	4	11-Mar-26	15-Mar-26	05-Aug-26 A	26-Aug-26 A	18,922.54	18,922.54	18,922.54	100%	100%	-135
JDH4-02-007-C	Pipe with diameter 600 mm pipe [De	4	25-Dec-25	29-Dec-25	25-Dec-25 A	29-Dec-25 A	14,128.83	14,128.83	14,128.83	100%	100%	0
JDH4-02-007-C	Pipe with diameter 800 mm pipe [De	4	25-Dec-25	29-Dec-25	25-Dec-25 A	29-Dec-25 A	14,191.91	14,191.91	14,191.91	100%	100%	0
Demolition in Sewerage network		4	25-Dec-25	29-Dec-25	25-Dec-25 A	29-Dec-25 A	93,225.07	93,225.07	93,225.07	100%	100%	0
JDH4-02-007-C	Pipe with diameter 200 mm pipe with	4	25-Dec-25	29-Dec-25	25-Dec-25 A	29-Dec-25 A	26,491.56	26,491.56	26,491.56	100%	100%	0
JDH4-02-007-C	Pipe with diameter 250 mm pipe with	4	25-Dec-25	29-Dec-25	25-Dec-25 A	29-Dec-25 A	38,349.69	38,349.69	38,349.69	100%	100%	0

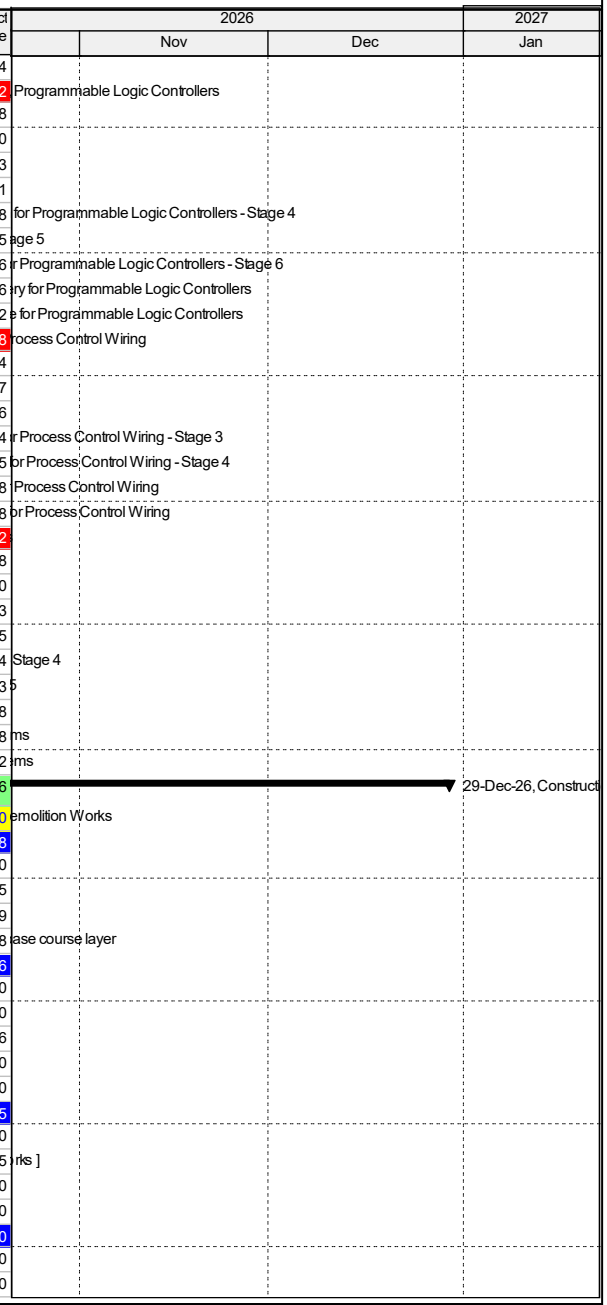


Date	Revision	Checked	Approved

Activity ID	Activity Name	Original Duration	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Schedule % Complete	Performance % Complete	Variance - BL Project Finish Date
JDH4-02-007-C	Manhole with depth 1.50m - 2.50m [[	4	25-Dec-25	29-Dec-25	25-Dec-25A	29-Dec-25A	12,615.03	12,615.03	12,615.03	100%	100%	0
JDH4-02-007-C	Manhole with depth 4.50m - 5.50m [[	4	25-Dec-25	29-Dec-25	25-Dec-25A	29-Dec-25A	15,768.79	15,768.79	15,768.79	100%	100%	0
Demolition in Potable water network		4	25-Dec-25	29-Dec-25	25-Dec-25A	29-Dec-25A	46,990.99	46,990.99	46,990.99	100%	100%	0
JDH4-02-007-C	Single house connection dia 63 mm	4	25-Dec-25	29-Dec-25	25-Dec-25A	29-Dec-25A	15,768.79	15,768.79	15,768.79	100%	100%	0
JDH4-02-007-C	Pipe with diameter 200 mm [Demoli	4	25-Dec-25	29-Dec-25	25-Dec-25A	29-Dec-25A	15,453.41	15,453.41	15,453.41	100%	100%	0
JDH4-02-007-C	Wash out valve with chamber; on 20	4	25-Dec-25	29-Dec-25	25-Dec-25A	29-Dec-25A	15,768.79	15,768.79	15,768.79	100%	100%	0
Demolition in Electrical works		155	25-Dec-25	07-Jun-26	25-Dec-25A	04-Oct-26A	89,194.45	89,194.45	89,194.45	100%	100%	-100
JDH4-02-007-C	Demolishing of existing Lighting Pole	33	25-Dec-25	01-Feb-26	25-Dec-25A	01-Feb-26A	17,002.05	17,002.05	17,002.05	100%	100%	0
JDH4-02-007-C	Demolishing of existing Lighting Pole	14	16-Mar-26	04-Apr-26	04-Feb-26A	10-Feb-26A	3,812.75	3,812.75	3,812.75	100%	100%	41
JDH4-02-007-C	Relocating of existing Lighting Pole [I	15	15-Jan-26	01-Feb-26	15-Jan-26A	01-Feb-26A	14,036.17	14,036.17	14,036.17	100%	100%	0
JDH4-02-007-C	Relocating of existing Lighting Pole [I	16	16-Mar-26	06-Apr-26	02-Feb-26A	03-Oct-26A	27,536.54	27,536.54	27,536.54	100%	100%	-149
JDH4-02-007-C	Relocating of existing Lighting Pole [I	16	07-Apr-26	25-Apr-26	16-Feb-26A	27-Aug-26A	4,730.64	4,730.64	4,730.64	100%	100%	-103
JDH4-02-007-C	Relocating of existing Lighting Pole [I	16	26-Apr-26	13-May-26	15-Feb-26A	19-Aug-26A	12,615.03	12,615.03	12,615.03	100%	100%	-80
JDH4-02-007-C	Relocating of existing Lighting Pole [I	18	14-May-26	07-Jun-26	18-Feb-26A	04-Oct-26A	9,461.27	9,461.27	9,461.27	100%	100%	-100
Plots		146	11-Dec-25	23-Mar-26	11-Dec-25A	06-Jul-26A	4,337,407.52	4,337,407.52	4,337,407.52	100%	100%	-87
Excavation		8	11-Mar-26	23-Mar-26	03-Feb-26A	02-Jul-26A	282,577.06	282,577.06	282,577.06	100%	100%	-84
JDH4-02-007-C	Plots excavation [Plots]	8	11-Mar-26	23-Mar-26	03-Feb-26A	02-Jul-26A	282,577.06	282,577.06	282,577.06	100%	100%	-84
Backfilling		146	11-Dec-25	23-Mar-26	11-Dec-25A	06-Jul-26A	4,054,830.46	4,054,830.46	4,054,830.46	100%	100%	-87
JDH4-02-007-C	Plots backfilling Stage 1 [Plots]	36	11-Dec-25	21-Jan-26	11-Dec-25A	21-Jan-26A	1,013,707.62	1,013,707.62	1,013,707.62	100%	100%	0
JDH4-02-007-C	Plots backfilling Stage 2 [Plots](Com	9	22-Jan-26	01-Feb-26	22-Jan-26A	01-Feb-26A	709,608.44	709,608.44	709,608.44	100%	100%	0
JDH4-02-007-C	Plots backfilling Stage 2 [Plots]	15	03-Feb-26	19-Feb-26	02-Feb-26A	12-Apr-26A	304,109.26	304,109.26	304,109.26	100%	100%	-40
JDH4-02-007-C	Plots backfilling Stage 3 [Plots](Com	3	29-Jan-26	01-Feb-26	29-Jan-26A	01-Feb-26A	202,739.50	202,739.50	202,739.50	100%	100%	0
JDH4-02-007-C	Plots backfilling Stage 3 [Plots]	10	21-Feb-26	04-Mar-26	02-Feb-26A	02-May-26A	810,958.02	810,958.02	810,958.02	100%	100%	-47
JDH4-02-007-C	Plots backfilling Stage 4 [Plots]	13	05-Mar-26	23-Mar-26	03-May-26A	06-Jul-26A	1,013,707.62	1,013,707.62	1,013,707.62	100%	100%	-87
Roads		453	04-Dec-25	24-Apr-27	04-Dec-25A	03-Nov-26	17,638,653.39	21,979,076.65	21,997,203.90	80.19%	99.92%	143
Road 04-R		416	03-Jan-26	24-Apr-27	03-Jan-26A	26-Sep-26A	3,716,049.04	5,772,635.72	5,772,635.72	64.37%	100%	177
Box Culvert		97	17-Jan-26	09-May-26	17-Jan-26A	20-Apr-26A	499,735.96	499,735.96	499,735.96	100%	100%	16
JDH4-02-007-	Excavation For Box Culvert [Road 04	9	17-Jan-26	26-Jan-26	17-Jan-26A	26-Jan-26A	47,552.35	47,552.35	47,552.35	100%	100%	0
JDH4-02-007-	Backfilling For Box Culvert [Road 04-	3	29-Jan-26	01-Feb-26	29-Jan-26A	01-Feb-26A	30,578.83	30,578.83	30,578.83	100%	100%	0
JDH4-02-007-	Plain Concrete for box culvert [Road	1	01-Feb-26	01-Feb-26	01-Feb-26A	01-Feb-26A	19,679.44	19,679.44	19,679.44	100%	100%	0
JDH4-02-007-	Steel Reinforcement for box culverts	1	01-Feb-26	01-Feb-26	01-Feb-26A	01-Feb-26A	33,891.12	33,891.12	33,891.12	100%	100%	0
JDH4-02-007-	Steel Reinforcement for box culverts	12	05-Apr-26	18-Apr-26	02-Feb-26A	19-Apr-26A	135,564.48	135,564.48	135,564.48	100%	100%	-1
JDH4-02-007-	Reinforced Concrete for box culvert	18	19-Apr-26	09-May-26	17-Feb-26A	20-Apr-26A	232,469.74	232,469.74	232,469.74	100%	100%	16
Road Works + Roundabout		416	03-Jan-26	17-Mar-27	03-Jan-26A	26-Sep-26A	2,484,514.26	3,655,865.47	3,655,865.47	67.96%	100%	145
Eartworks & Site grading		199	03-Jan-26	22-Jun-26	03-Jan-26A	08-Jun-26A	1,552,916.51	1,552,916.51	1,552,916.51	100%	100%	13
JDH4-02-007	Road excavation [Road 04-R](Com	8	24-Jan-26	01-Feb-26	24-Jan-26A	01-Feb-26A	14,012.87	14,012.87	14,012.87	100%	100%	0
JDH4-02-007	Road excavation [Road 04-R]	16	10-May-26	31-May-26	03-Feb-26A	14-May-26A	21,019.30	21,019.30	21,019.30	100%	100%	12
JDH4-02-007	Road backfilling [Road 04-R](Comp	26	03-Jan-26	01-Feb-26	03-Jan-26A	01-Feb-26A	551,521.49	551,521.49	551,521.49	100%	100%	0
JDH4-02-007	Road backfilling [Road 04-R]	16	16-May-26	06-Jun-26	02-Feb-26A	14-May-26A	827,282.24	827,282.24	827,282.24	100%	100%	17
JDH4-02-007	Subgrade [Road 04-R]	13	08-Jun-26	22-Jun-26	30-Apr-26A	08-Jun-26A	139,080.60	139,080.60	139,080.60	100%	100%	13
Asphalt Works		40	04-Jul-26	24-Aug-26	11-Jun-26A	18-Jun-26A	931,597.75	931,597.75	931,597.75	100%	100%	58
JDH4-02-007	Aggregate base course [Road 04-R	16	04-Jul-26	21-Jul-26	11-Jun-26A	14-Jun-26A	141,644.69	141,644.69	141,644.69	100%	100%	33
JDH4-02-007	Prime Coat (MC1) [Road 04-R]	14	22-Jul-26	06-Aug-26	14-Jun-26A	17-Jun-26A	78,995.31	78,995.31	78,995.31	100%	100%	44
JDH4-02-007	Bituminous base course [Road 04-R	11	09-Aug-26	24-Aug-26	17-Jun-26A	18-Jun-26A	710,957.75	710,957.75	710,957.75	100%	100%	58
Finishing Works		97	17-Jan-27	17-Mar-27	17-Jun-26A	26-Sep-26A	0.00	1,171,351.21	1,171,351.21	0%	100%	145
Asphalt Wearing Course		28	17-Jan-27	17-Feb-27	12-Sep-26A	15-Sep-26A	0.00	418,188.18	418,188.18	0%	100%	132
JDH4-02-00	Tack Coat (RC2) [Road 04-R]	12	17-Jan-27	30-Jan-27	12-Sep-26A	15-Sep-26A	0.00	41,818.82	41,818.82	0%	100%	116
JDH4-02-00	Bituminous concrete wearing course	16	31-Jan-27	17-Feb-27	12-Sep-26A	14-Sep-26A	0.00	376,369.36	376,369.36	0%	100%	133
Precast Concrete Curb		5	18-Feb-27	24-Feb-27	30-Jul-26A	01-Aug-26A	0.00	260,761.75	260,761.75	0%	100%	176
JDH4-02-00	Installation of Precast Concrete curb	5	18-Feb-27	24-Feb-27	30-Jul-26A	01-Aug-26A	0.00	260,761.75	260,761.75	0%	100%	176
Precast Interlocking block pavers		15	25-Feb-27	17-Mar-27	02-Aug-26A	04-Aug-26A	0.00	247,979.91	247,979.91	0%	100%	188

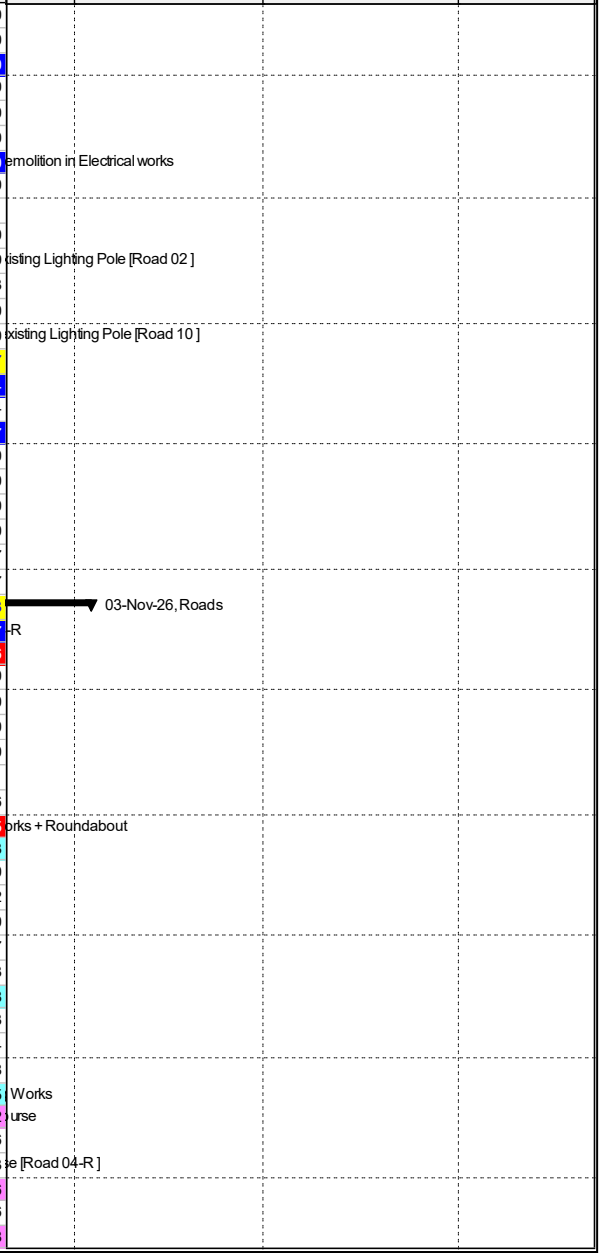

Date	Revision	Checked	Approved

Activity ID	Activity Name	Original Duration	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Schedule % Complete	Performance % Complete	Variance - BL Project Finish Date
JDH4-02-00	Installation of Interlocking block pave	15	25-Feb-27	17-Mar-27	02-Aug-26 A	04-Aug-26 A	0.00	247,979.91	247,979.91	0%	100%	188
Pavement Markings		9	18-Feb-27	01-Mar-27	24-Sep-26 A	26-Sep-26 A	0.00	70,108.71	70,108.71	0%	100%	134
JDH4-02-00	Pavement markings [Road 04-R]	9	18-Feb-27	01-Mar-27	24-Sep-26 A	26-Sep-26 A	0.00	70,108.71	70,108.71	0%	100%	134
Traffic Signage		15	18-Feb-27	08-Mar-27	30-Jul-26 A	11-Sep-26 A	0.00	119,121.91	119,121.91	0%	100%	151
JDH4-02-00	Installation of Traffic Signs [Road 04-F	15	18-Feb-27	08-Mar-27	30-Jul-26 A	11-Sep-26 A	0.00	119,121.91	119,121.91	0%	100%	151
Guardrail		21	31-Jan-27	24-Feb-27	17-Jun-26 A	25-Jun-26 A	0.00	55,190.75	55,190.75	0%	100%	207
JDH4-02-00	Installation of Guard rails [Road 04-R	21	31-Jan-27	24-Feb-27	17-Jun-26 A	25-Jun-26 A	0.00	55,190.75	55,190.75	0%	100%	207
Storm Water Drainage		322	07-Jan-26	14-Dec-26	07-Jan-26 A	22-Jul-26 A	327,706.48	616,227.34	616,227.34	53.18%	100%	123
Pipe Works		269	07-Jan-26	17-Nov-26	07-Jan-26 A	20-Apr-26 A	327,706.48	372,950.21	372,950.21	87.87%	100%	177
JDH4-02-007	Excavation and Compaction (FDT) [I	22	07-Jan-26	01-Feb-26	07-Jan-26 A	01-Feb-26 A	13,055.44	13,055.44	13,055.44	100%	100%	0
JDH4-02-007	Excavation and Compaction (FDT) [I	18	25-Aug-26	14-Sep-26	03-Feb-26 A	09-Apr-26 A	24,245.82	24,245.82	24,245.82	100%	100%	133
JDH4-02-007	Sand Bedding [Road 04-R](Compl	21	08-Jan-26	01-Feb-26	08-Jan-26 A	01-Feb-26 A	6,527.73	6,527.73	6,527.73	100%	100%	0
JDH4-02-007	Sand Bedding [Road 04-R]	9	15-Sep-26	26-Sep-26	03-Feb-26 A	11-Apr-26 A	12,122.92	12,122.92	12,122.92	100%	100%	141
JDH4-02-007	Installation of GRP Pipe [Road 04-R	20	10-Jan-26	01-Feb-26	10-Jan-26 A	01-Feb-26 A	91,388.14	91,388.14	91,388.14	100%	100%	0
JDH4-02-007	Installation of GRP Pipe [Road 04-R	17	27-Sep-26	15-Oct-26	03-Feb-26 A	18-Apr-26 A	169,720.83	169,720.83	169,720.83	100%	100%	151
JDH4-02-007	Sand Cover & Warning Tape [Road	7	17-Oct-26	24-Oct-26	29-Jan-26 A	19-Apr-26 A	10,645.59	18,629.79	18,629.79	57.14%	100%	157
JDH4-02-007	Backfilling & Compaction [Road 04-F	21	25-Oct-26	17-Nov-26	01-Feb-26 A	20-Apr-26 A	0.00	37,259.53	37,259.53	0%	100%	177
Pipe Encasement		5	18-Nov-26	23-Nov-26	29-Jan-26 A	19-Apr-26 A	0.00	13,406.24	13,406.24	0%	100%	183
JDH4-02-007	Pipe Encasement Works [Road 04-I	5	18-Nov-26	23-Nov-26	29-Jan-26 A	19-Apr-26 A	0.00	13,406.24	13,406.24	0%	100%	183
Manholes		6	24-Nov-26	30-Nov-26	01-Feb-26 A	04-Apr-26 A	0.00	130,842.92	130,842.92	0%	100%	202
JDH4-02-007	Installation of Precast Manhole Ring	6	24-Nov-26	30-Nov-26	01-Feb-26 A	04-Apr-26 A	0.00	130,842.92	130,842.92	0%	100%	202
Precast Access Opening		4	01-Dec-26	05-Dec-26	07-Jul-26 A	22-Jul-26 A	0.00	7,569.02	7,569.02	0%	100%	115
JDH4-02-007	Installation of Precast Access Openin	4	01-Dec-26	05-Dec-26	07-Jul-26 A	22-Jul-26 A	0.00	7,569.02	7,569.02	0%	100%	115
Catch Basins		5	06-Dec-26	10-Dec-26	28-Apr-26 A	09-May-26 A	0.00	40,998.84	40,998.84	0%	100%	181
JDH4-02-007	Construction of Catch basins [Road (	5	06-Dec-26	10-Dec-26	28-Apr-26 A	09-May-26 A	0.00	40,998.84	40,998.84	0%	100%	181
Concrete Outfalls		8	06-Dec-26	14-Dec-26	17-Jun-26 A	29-Jun-26 A	0.00	50,460.11	50,460.11	0%	100%	143
JDH4-02-007	Construction of Concrete outfall struc	8	06-Dec-26	14-Dec-26	17-Jun-26 A	29-Jun-26 A	0.00	50,460.11	50,460.11	0%	100%	143
Sewerage Network		200	29-Jan-26	11-Jul-26	29-Jan-26 A	20-Apr-26 A	233,847.07	233,847.07	233,847.07	100%	100%	68
Pipe Works		171	29-Jan-26	11-Jul-26	29-Jan-26 A	20-Apr-26 A	151,982.41	151,982.41	151,982.41	100%	100%	68
JDH4-02-007	Excavation & Compaction (FDT) [Ro	3	29-Jan-26	01-Feb-26	29-Jan-26 A	01-Feb-26 A	759.81	759.81	759.81	100%	100%	0
JDH4-02-007	Excavation & Compaction (FDT) [Ro	7	08-Jun-26	15-Jun-26	26-Mar-26 A	12-Apr-26 A	14,436.45	14,436.45	14,436.45	100%	100%	52
JDH4-02-007	Sand Bedding [Road 04-R]	7	16-Jun-26	23-Jun-26	31-Mar-26 A	13-Apr-26 A	7,599.22	7,599.22	7,599.22	100%	100%	58
JDH4-02-007	Installation of GRP Pipe [Road 04-R	9	24-Jun-26	04-Jul-26	31-Mar-26 A	18-Apr-26 A	75,992.31	75,992.31	75,992.31	100%	100%	64
JDH4-02-007	Gravity Test [Road 04-R]	3	05-Jul-26	07-Jul-26	02-Apr-26 A	19-Apr-26 A	30,396.93	30,396.93	30,396.93	100%	100%	66
JDH4-02-007	Sand Cover & Warning Tape [Road	4	05-Jul-26	08-Jul-26	04-Apr-26 A	20-Apr-26 A	7,599.22	7,599.22	7,599.22	100%	100%	66
JDH4-02-007	Backfilling & Compaction [Road 04-F	6	05-Jul-26	11-Jul-26	06-Apr-26 A	20-Apr-26 A	15,198.47	15,198.47	15,198.47	100%	100%	68
Pipe Encasement		7	24-Jun-26	01-Jul-26	04-Apr-26 A	20-Apr-26 A	760.54	760.54	760.54	100%	100%	60
JDH4-02-007	Pipe Encasement Works [Road 04-I	7	24-Jun-26	01-Jul-26	04-Apr-26 A	20-Apr-26 A	760.54	760.54	760.54	100%	100%	60
Manholes		7	24-Jun-26	01-Jul-26	28-Mar-26 A	05-Apr-26 A	81,104.12	81,104.12	81,104.12	100%	100%	73
JDH4-02-007	Installation of Manholes [Road 04-R]	7	24-Jun-26	01-Jul-26	28-Mar-26 A	05-Apr-26 A	81,104.12	81,104.12	81,104.12	100%	100%	73
TSE Network		56	25-Aug-26	17-Nov-26	25-Mar-26 A	23-May-26 A	146,003.55	186,231.54	186,231.54	78.4%	100%	150
Pipe Works		53	25-Aug-26	26-Oct-26	25-Mar-26 A	20-Apr-26 A	146,003.55	160,003.08	160,003.08	91.25%	100%	159
JDH4-02-007	Excavation and Compaction (FDT) [I	12	25-Aug-26	07-Sep-26	25-Mar-26 A	15-Apr-26 A	15,169.19	15,169.19	15,169.19	100%	100%	122
JDH4-02-007	Sand Bedding [Road 04-R]	9	08-Sep-26	17-Sep-26	28-Mar-26 A	16-Apr-26 A	7,584.62	7,584.62	7,584.62	100%	100%	130
JDH4-02-007	Installation of HDPE Pipe [Road 04-	12	19-Sep-26	03-Oct-26	30-Mar-26 A	18-Apr-26 A	75,846.00	75,846.00	75,846.00	100%	100%	141
JDH4-02-007	Initial Pressure Test [Road 04-R]	3	04-Oct-26	06-Oct-26	01-Apr-26 A	18-Apr-26 A	30,338.38	30,338.38	30,338.38	100%	100%	144
JDH4-02-007	Sand Cover & Warning [Road 04-R	7	07-Oct-26	14-Oct-26	02-Apr-26 A	19-Apr-26 A	7,584.62	7,584.62	7,584.62	100%	100%	150
JDH4-02-007	Backfilling & Compaction [Road 04-F	8	15-Oct-26	24-Oct-26	04-Apr-26 A	20-Apr-26 A	9,480.74	15,169.19	15,169.19	62.5%	100%	157
JDH4-02-007	Point of Connection [Road 04-R]	2	25-Oct-26	26-Oct-26	06-Apr-26 A	20-Apr-26 A	0.00	8,311.08	8,311.08	0%	100%	159
Pipe Encasement		12	27-Oct-26	09-Nov-26	02-Apr-26 A	19-Apr-26 A	0.00	7,554.90	7,554.90	0%	100%	172
JDH4-02-007	Encasement for Pipes [Road 04-R]	12	27-Oct-26	09-Nov-26	02-Apr-26 A	19-Apr-26 A	0.00	7,554.90	7,554.90	0%	100%	172

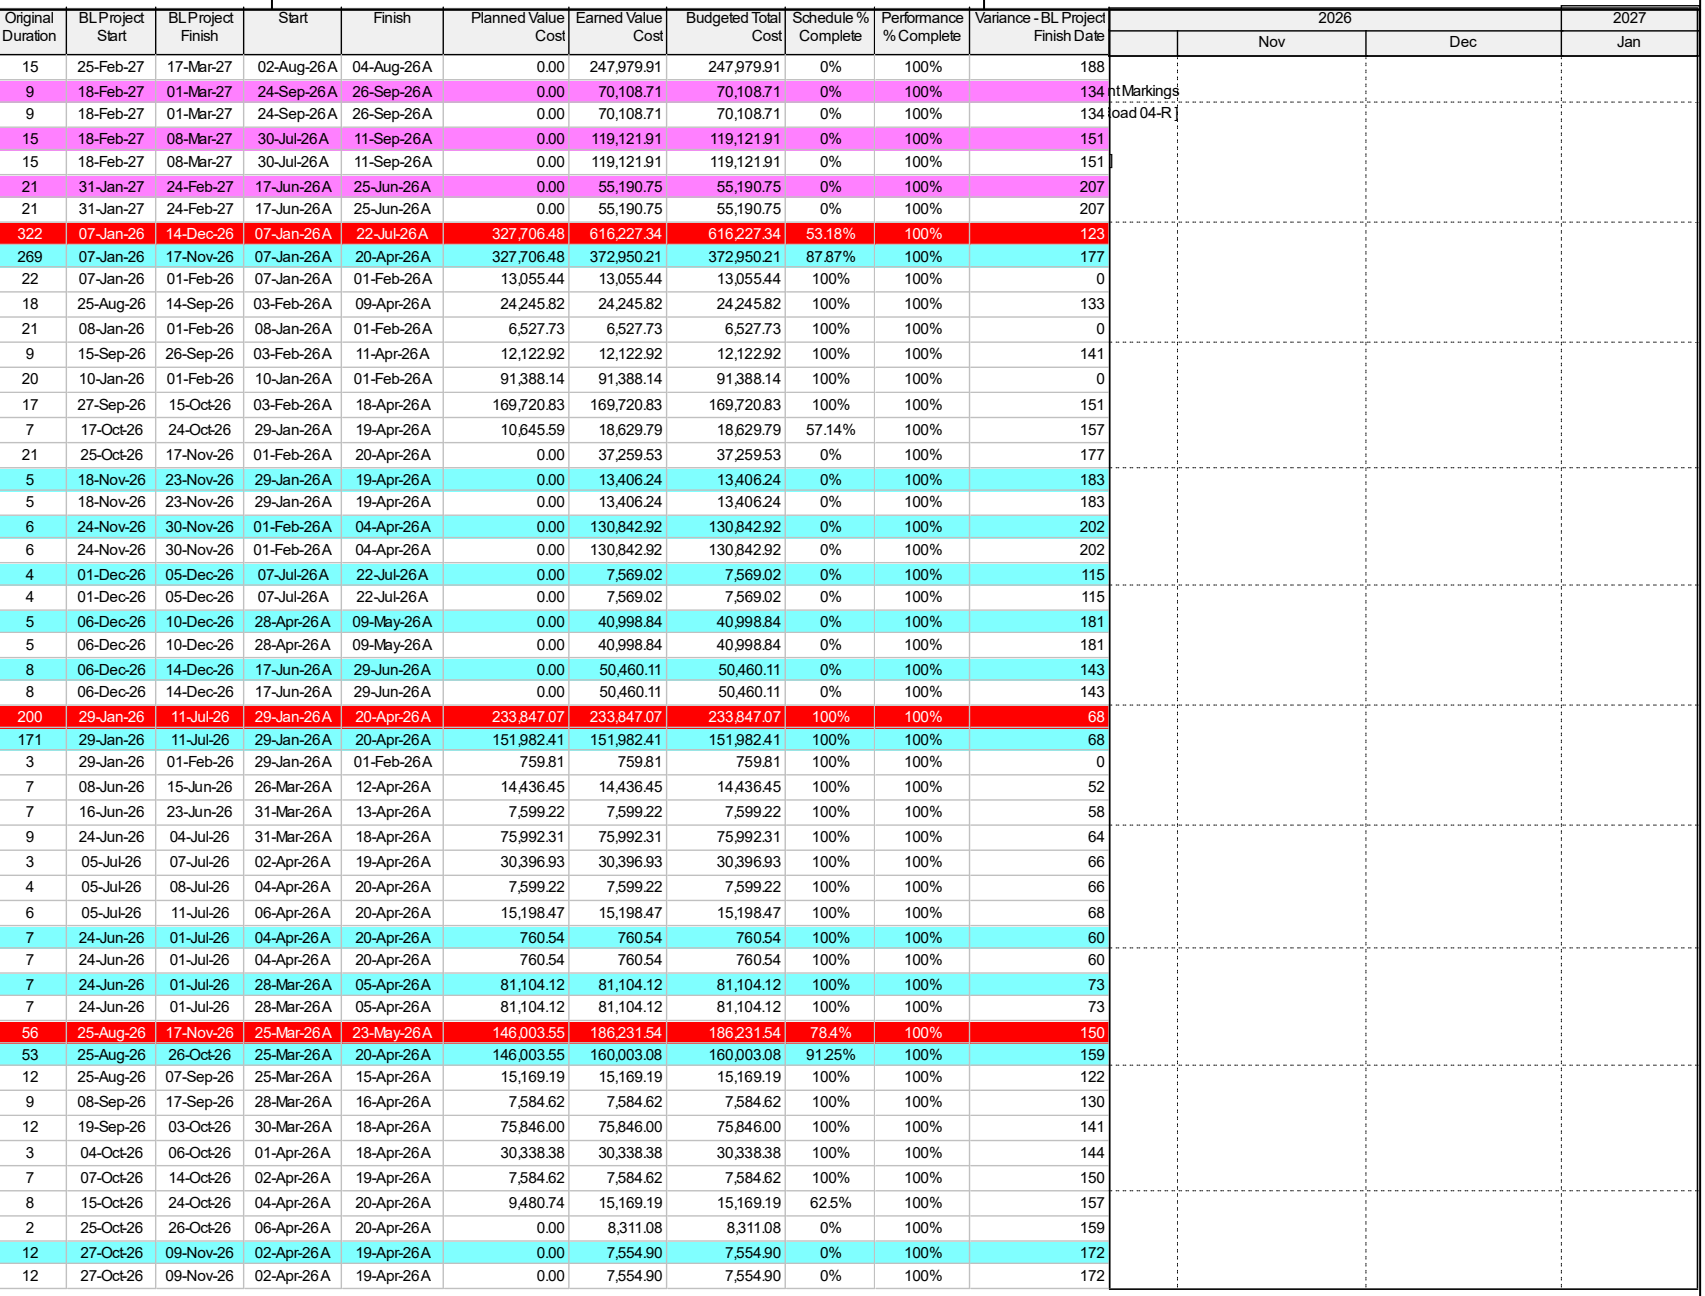

Date	Revision	Checked	Approved

Activity ID	Activity Name	Original Duration	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Schedule % Complete	Performance % Complete	Variance - BL Project Finish Date
Valves		7	10-Nov-26	17-Nov-26	16-Apr-26 A	23-May-26 A	0.00	18,673.56	18,673.56	0%	100%	150
JDH4-02-007	Installation of Gate Valves [Road 04-I	7	10-Nov-26	17-Nov-26	16-Apr-26 A	23-May-26 A	0.00	18,673.56	18,673.56	0%	100%	150
Potable Network		84	27-Sep-26	23-Nov-26	23-Mar-26 A	25-May-26 A	24,241.71	193,744.83	193,744.83	12.51%	100%	153
Pipe Works		63	27-Sep-26	19-Nov-26	23-Mar-26 A	25-May-26 A	24,241.71	124,027.28	124,027.28	19.55%	100%	150
JDH4-02-007	Excavation and Compaction (FDT) [I	12	27-Sep-26	10-Oct-26	23-Mar-26 A	15-Apr-26 A	12,402.74	12,402.74	12,402.74	100%	100%	149
JDH4-02-007	Sand Bedding [Road 04-R]	8	11-Oct-26	19-Oct-26	26-Mar-26 A	16-Apr-26 A	6,201.37	6,201.37	6,201.37	100%	100%	156
JDH4-02-007	Installation of HDPE Pipe [Road 04-	11	20-Oct-26	01-Nov-26	31-Mar-26 A	21-May-26 A	5,637.60	62,013.62	62,013.62	9.09%	100%	137
JDH4-02-007	Initial Pressure Test [Road 04-R]	3	02-Nov-26	04-Nov-26	02-Apr-26 A	23-May-26 A	0.00	24,805.44	24,805.44	0%	100%	139
JDH4-02-007	Sand Cover & Warning Tape [Road	6	05-Nov-26	11-Nov-26	04-Apr-26 A	24-May-26 A	0.00	6,201.37	6,201.37	0%	100%	144
JDH4-02-007	Backfilling [Road 04-R]	7	12-Nov-26	19-Nov-26	06-Apr-26 A	25-May-26 A	0.00	12,402.74	12,402.74	0%	100%	150
Pipe Encasement		5	02-Nov-26	07-Nov-26	04-Apr-26 A	24-May-26 A	0.00	9,796.16	9,796.16	0%	100%	140
JDH4-02-007	Encasement for Pipes [Road 04-R]	5	02-Nov-26	07-Nov-26	04-Apr-26 A	24-May-26 A	0.00	9,796.16	9,796.16	0%	100%	140
Valves		7	08-Nov-26	15-Nov-26	15-Apr-26 A	19-Apr-26 A	0.00	15,768.79	15,768.79	0%	100%	177
JDH4-02-007	Installation of Gate Valves [Road 04-I	7	08-Nov-26	15-Nov-26	15-Apr-26 A	19-Apr-26 A	0.00	15,768.79	15,768.79	0%	100%	177
Fire Hydrant		5	18-Nov-26	23-Nov-26	29-Apr-26 A	10-May-26 A	0.00	44,152.60	44,152.60	0%	100%	166
JDH4-02-007	Installation of 3-outlet fire hydrant [Ro	5	18-Nov-26	23-Nov-26	29-Apr-26 A	10-May-26 A	0.00	44,152.60	44,152.60	0%	100%	166
Electrical Works		149	24-Nov-26	24-Apr-27	07-Jun-26 A	24-Sep-26 A	0.00	386,983.51	386,983.51	0%	100%	178 Works
Street Lighting		114	24-Nov-26	01-Mar-27	07-Jun-26 A	24-Sep-26 A	0.00	173,158.79	173,158.79	0%	100%	135 ting
JDH4-02-007	Excavation for Low Voltage Cable [R	15	24-Nov-26	10-Dec-26	10-Jun-26 A	10-Aug-26 A	0.00	9,991.10	9,991.10	0%	100%	105
JDH4-02-007	Installation of Road Crossing Ducts [I	13	12-Dec-26	26-Dec-26	07-Jun-26 A	11-Jun-26 A	0.00	17,941.62	17,941.62	0%	100%	168
JDH4-02-007	Installation of Low Voltage Cables [R	16	27-Dec-26	13-Jan-27	13-Jun-26 A	12-Aug-26 A	0.00	50,825.95	50,825.95	0%	100%	131
JDH4-02-007	Installation of Lighting Poles [Road 0	12	14-Jan-27	27-Jan-27	21-Jul-26 A	15-Aug-26 A	0.00	73,193.61	73,193.61	0%	100%	142
JDH4-02-007	Installation of Lighting Luminaires [R	12	28-Jan-27	10-Feb-27	25-Jul-26 A	16-Aug-26 A	0.00	17,422.00	17,422.00	0%	100%	153
JDH4-02-007	Installation of Earthing System [Road	15	11-Feb-27	01-Mar-27	15-Aug-26 A	24-Sep-26 A	0.00	3,784.51	3,784.51	0%	100%	135 stem [Road 04-R]
Telecommunication		28	02-Mar-27	24-Apr-27	16-Jun-26 A	17-Aug-26 A	0.00	213,824.72	213,824.72	0%	100%	209
JDH4-02-007	Installation Road Crossing R/F 6 way	14	02-Mar-27	21-Mar-27	16-Jun-26 A	05-Aug-26 A	0.00	182,034.85	182,034.85	0%	100%	191
JDH4-02-007	Installation Road Crossing Un R/F 6	14	22-Mar-27	06-Apr-27	16-Jun-26 A	22-Jun-26 A	0.00	3,406.06	3,406.06	0%	100%	242
JDH4-02-007	Installation of Manholes [Road 04-R]	15	07-Apr-27	24-Apr-27	22-Jul-26 A	17-Aug-26 A	0.00	28,383.81	28,383.81	0%	100%	209
Road 08		448	10-Dec-25	31-Mar-27	10-Dec-25 A	03-Oct-26 A	4,696,852.74	5,696,664.36	5,696,664.36	82.45%	100%	150 ad 08
Road Works + Roundabout		448	10-Dec-25	31-Mar-27	10-Dec-25 A	24-Sep-26 A	2,203,585.53	3,190,850.42	3,190,850.42	69.06%	100%	158 ks + Roundabout
Eartworks & Site grading		224	10-Dec-25	17-Aug-26	10-Dec-25 A	03-May-26 A	1,378,559.54	1,378,559.54	1,378,559.54	100%	100%	88
JDH4-02-007	Road excavation [Road 08](Compl	46	10-Dec-25	01-Feb-26	10-Dec-25 A	01-Feb-26 A	21,754.74	21,754.74	21,754.74	100%	100%	0
JDH4-02-007	Road excavation [Road 08]	14	04-Feb-26	19-Feb-26	04-Mar-26 A	09-Apr-26 A	9,323.46	9,323.46	9,323.46	100%	100%	-38
JDH4-02-007	Road backfilling [Road 08](Complet	44	13-Dec-25	01-Feb-26	13-Dec-25 A	01-Feb-26 A	673,400.08	673,400.08	673,400.08	100%	100%	0
JDH4-02-007	Road backfilling [Road 08]	14	21-Feb-26	09-Mar-26	03-Feb-26 A	12-Apr-26 A	550,963.70	550,963.70	550,963.70	100%	100%	-25
JDH4-02-007	Subgrade [Road 08]	10	06-Aug-26	17-Aug-26	16-Apr-26 A	03-May-26 A	123,117.55	123,117.55	123,117.55	100%	100%	88
Asphalt Works		34	18-Aug-26	20-Sep-26	29-Apr-26 A	16-May-26 A	825,025.99	825,025.99	825,025.99	100%	100%	106
JDH4-02-007	Aggregate base course [Road 08]	10	18-Aug-26	29-Aug-26	29-Apr-26 A	12-May-26 A	125,409.15	125,409.15	125,409.15	100%	100%	91
JDH4-02-007	Prime Coat (MC1) [Road 08]	7	30-Aug-26	06-Sep-26	30-Apr-26 A	13-May-26 A	70,000.79	70,000.79	70,000.79	100%	100%	97
JDH4-02-007	Bituminous base course [Road 08]	12	07-Sep-26	20-Sep-26	02-May-26 A	16-May-26 A	629,616.05	629,616.05	629,616.05	100%	100%	106
Finishing Works		100	31-Jan-27	31-Mar-27	12-May-26 A	24-Sep-26 A	0.00	987,264.89	987,264.89	0%	100%	158 Works
Asphalt Wearing Course		32	31-Jan-27	09-Mar-27	09-Sep-26 A	12-Sep-26 A	0.00	370,629.53	370,629.53	0%	100%	151 se
JDH4-02-00	Tack Coat (RC2) [Road 08]	16	31-Jan-27	17-Feb-27	09-Sep-26 A	12-Sep-26 A	0.00	36,898.96	36,898.96	0%	100%	135
JDH4-02-00	Bituminous concrete wearing course	16	18-Feb-27	09-Mar-27	10-Sep-26 A	12-Sep-26 A	0.00	333,730.57	333,730.57	0%	100%	151 [Road 08]
Precast Concrete Curb		10	14-Mar-27	24-Mar-27	12-May-26 A	01-Jul-26 A	0.00	231,115.34	231,115.34	0%	100%	223
JDH4-02-00	Installation of Precast Concrete curb	10	14-Mar-27	24-Mar-27	12-May-26 A	01-Jul-26 A	0.00	231,115.34	231,115.34	0%	100%	223
Precast Interlocking block pavers		10	14-Mar-27	24-Mar-27	10-Jun-26 A	04-Jul-26 A	0.00	219,785.33	219,785.33	0%	100%	221
JDH4-02-00	Installation of Interlocking block pave	10	14-Mar-27	24-Mar-27	10-Jun-26 A	04-Jul-26 A	0.00	219,785.33	219,785.33	0%	100%	221
Pavement Markings		12	18-Mar-27	31-Mar-27	23-Sep-26 A	24-Sep-26 A	0.00	62,150.42	62,150.42	0%	100%	158 Markings
JDH4-02-00	Pavement markings [Road 08]	12	18-Mar-27	31-Mar-27	23-Sep-26 A	24-Sep-26 A	0.00	62,150.42	62,150.42	0%	100%	158 ad 08]
Traffic Signage		15	09-Mar-27	29-Mar-27	15-Jul-26 A	05-Sep-26 A	0.00	103,584.27	103,584.27	0%	100%	171

2026 | 2027


Nov | Dec | Jan

Actual Work | Critical Remaining Work

Remaining Work | Milestone

Date	Revision	Checked	Approved

Activity ID	Activity Name	Original Duration	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Schedule % Complete	Performance % Complete	Variance - BL Project Finish Date
JDH4-02-00	Installation of Traffic Signs [Road 08]	15	09-Mar-27	29-Mar-27	15-Jul-26 A	05-Sep-26 A	0.00	103,584.27	103,584.27	0%	100%	171
Storm Water Drainage		199	15-Jan-26	10-Jun-26	15-Jan-26 A	26-Aug-26 A	873,781.35	873,781.35	873,781.35	100%	100%	-66
Pipe Works		125	15-Jan-26	10-Jun-26	15-Jan-26 A	09-Mar-26 A	547,596.42	547,596.42	547,596.42	100%	100%	75
JDH4-02-007	Excavation and Compaction (FDT) [I	15	15-Jan-26	01-Feb-26	15-Jan-26 A	01-Feb-26 A	8,213.94	8,213.94	8,213.94	100%	100%	0
JDH4-02-007	Excavation and Compaction (FDT) [I	20	21-Feb-26	16-Mar-26	03-Feb-26 A	03-Mar-26 A	46,545.67	46,545.67	46,545.67	100%	100%	12
JDH4-02-007	Sand Bedding [Road 08](Complete	11	20-Jan-26	01-Feb-26	20-Jan-26 A	01-Feb-26 A	4,106.98	4,106.98	4,106.98	100%	100%	0
JDH4-02-007	Sand Bedding [Road 08]	11	17-Mar-26	01-Apr-26	03-Feb-26 A	03-Mar-26 A	23,272.86	23,272.86	23,272.86	100%	100%	22
JDH4-02-007	Installation of GRP Pipe [Road 08]((	11	20-Jan-26	01-Feb-26	20-Jan-26 A	01-Feb-26 A	57,497.63	57,497.63	57,497.63	100%	100%	0
JDH4-02-007	Installation of GRP Pipe [Road 08]	26	02-Apr-26	02-May-26	04-Feb-26 A	04-Mar-26 A	325,819.88	325,819.88	325,819.88	100%	100%	47
JDH4-02-007	Sand Cover & Warning Tape [Road	9	22-Jan-26	01-Feb-26	22-Jan-26 A	01-Feb-26 A	4,106.98	4,106.98	4,106.98	100%	100%	0
JDH4-02-007	Sand Cover & Warning Tape [Road	10	03-May-26	13-May-26	05-Feb-26 A	07-Mar-26 A	23,272.86	23,272.86	23,272.86	100%	100%	56
JDH4-02-007	Backfilling & Compaction [Road 08](	8	24-Jan-26	01-Feb-26	24-Jan-26 A	01-Feb-26 A	8,213.94	8,213.94	8,213.94	100%	100%	0
JDH4-02-007	Backfilling & Compaction [Road 08]	21	14-May-26	10-Jun-26	04-Feb-26 A	09-Mar-26 A	46,545.67	46,545.67	46,545.67	100%	100%	75
Pipe Encasement		5	03-May-26	07-May-26	05-Feb-26 A	07-Mar-26 A	20,926.82	20,926.82	20,926.82	100%	100%	51
JDH4-02-007	Pipe Encasement Works [Road 08]	5	03-May-26	07-May-26	05-Feb-26 A	07-Mar-26 A	20,926.82	20,926.82	20,926.82	100%	100%	51
Manholes		6	09-May-26	14-May-26	03-Feb-26 A	15-Feb-26 A	224,206.55	224,206.55	224,206.55	100%	100%	73
JDH4-02-007	Installation of Precast Manhole Ring [	6	09-May-26	14-May-26	03-Feb-26 A	15-Feb-26 A	224,206.55	224,206.55	224,206.55	100%	100%	73
Precast Access Opening		3	16-May-26	18-May-26	05-Aug-26 A	26-Aug-26 A	11,353.53	11,353.53	11,353.53	100%	100%	-83
JDH4-02-007	Installation of Precast Access Openin	3	16-May-26	18-May-26	05-Aug-26 A	26-Aug-26 A	11,353.53	11,353.53	11,353.53	100%	100%	-83
Catch Basins		9	19-May-26	01-Jun-26	26-Mar-26 A	18-Apr-26 A	69,698.03	69,698.03	69,698.03	100%	100%	35
JDH4-02-007	Construction of Catch basins [Road (	9	19-May-26	01-Jun-26	26-Mar-26 A	18-Apr-26 A	69,698.03	69,698.03	69,698.03	100%	100%	35
Sewerage Network		120	17-Mar-26	16-Jul-26	03-Feb-26 A	03-Mar-26 A	558,310.64	558,310.64	558,310.64	100%	100%	111
Pipe Works		88	17-Mar-26	25-Jun-26	03-Feb-26 A	03-Mar-26 A	329,545.92	329,545.92	329,545.92	100%	100%	93
JDH4-02-007	Excavation & Compaction (FDT) [Ro	18	17-Mar-26	09-Apr-26	03-Feb-26 A	25-Feb-26 A	32,954.60	32,954.60	32,954.60	100%	100%	35
JDH4-02-007	Sand Bedding [Road 08]	9	11-Apr-26	20-Apr-26	05-Feb-26 A	26-Feb-26 A	16,477.28	16,477.28	16,477.28	100%	100%	43
JDH4-02-007	Installation of GRP Pipe [Road 08]	9	21-Apr-26	30-Apr-26	09-Feb-26 A	28-Feb-26 A	164,772.96	164,772.96	164,772.96	100%	100%	51
JDH4-02-007	Gravity Test [Road 08]	17	02-May-26	20-May-26	11-Feb-26 A	28-Feb-26 A	65,909.20	65,909.20	65,909.20	100%	100%	68
JDH4-02-007	Sand Cover & Warning Tape [Road	7	21-May-26	01-Jun-26	12-Feb-26 A	01-Mar-26 A	16,477.28	16,477.28	16,477.28	100%	100%	74
JDH4-02-007	Backfilling & Compaction [Road 08]	21	02-Jun-26	25-Jun-26	14-Feb-26 A	03-Mar-26 A	32,954.60	32,954.60	32,954.60	100%	100%	93
Pipe Encasement		11	27-Jun-26	08-Jul-26	12-Feb-26 A	01-Mar-26 A	1,673.19	1,673.19	1,673.19	100%	100%	106
JDH4-02-007	Pipe Encasement Works [Road 08]	11	27-Jun-26	08-Jul-26	12-Feb-26 A	01-Mar-26 A	1,673.19	1,673.19	1,673.19	100%	100%	106
Manholes		7	09-Jul-26	16-Jul-26	08-Feb-26 A	03-Mar-26 A	227,091.53	227,091.53	227,091.53	100%	100%	111
JDH4-02-007	Installation of Manholes [Road 08]	7	09-Jul-26	16-Jul-26	08-Feb-26 A	03-Mar-26 A	227,091.53	227,091.53	227,091.53	100%	100%	111
TSE Network		93	11-Apr-26	09-Jul-26	03-Feb-26 A	09-May-26 A	229,231.81	229,231.81	229,231.81	100%	100%	50
Pipe Works		75	11-Apr-26	09-Jul-26	03-Feb-26 A	02-May-26 A	195,413.82	195,413.82	195,413.82	100%	100%	56
JDH4-02-007	Excavation and Compaction (FDT) [I	18	11-Apr-26	30-Apr-26	03-Feb-26 A	14-Apr-26 A	18,710.26	18,710.26	18,710.26	100%	100%	14
JDH4-02-007	Sand Bedding [Road 08]	11	02-May-26	13-May-26	07-Feb-26 A	15-Apr-26 A	9,355.16	9,355.16	9,355.16	100%	100%	24
JDH4-02-007	Installation of HDPE Pipe [Road 08]	20	14-May-26	09-Jun-26	08-Feb-26 A	29-Apr-26 A	93,551.37	93,551.37	93,551.37	100%	100%	32
JDH4-02-007	Initial Pressure Test [Road 08]	8	10-Jun-26	18-Jun-26	12-Feb-26 A	30-Apr-26 A	37,420.53	37,420.53	37,420.53	100%	100%	39
JDH4-02-007	Sand Cover & Warning [Road 08]	8	20-Jun-26	28-Jun-26	14-Feb-26 A	02-May-26 A	9,355.16	9,355.16	9,355.16	100%	100%	46
JDH4-02-007	Backfilling & Compaction [Road 08]	10	29-Jun-26	09-Jul-26	15-Feb-26 A	02-May-26 A	18,710.26	18,710.26	18,710.26	100%	100%	56
JDH4-02-007	Point of Connection [Road 08]	5	10-Jun-26	15-Jun-26	18-Apr-26 A	02-May-26 A	8,311.08	8,311.08	8,311.08	100%	100%	35
Pipe Encasement		7	10-Jun-26	17-Jun-26	14-Feb-26 A	02-May-26 A	9,368.07	9,368.07	9,368.07	100%	100%	37
JDH4-02-007	Encasement for Pipes [Road 08]	7	10-Jun-26	17-Jun-26	14-Feb-26 A	02-May-26 A	9,368.07	9,368.07	9,368.07	100%	100%	37
Valves		7	18-Jun-26	25-Jun-26	15-Mar-26 A	09-May-26 A	11,204.14	11,204.14	11,204.14	100%	100%	38
JDH4-02-007	Installation of Gate Valves [Road 08]	7	18-Jun-26	25-Jun-26	15-Mar-26 A	09-May-26 A	11,204.14	11,204.14	11,204.14	100%	100%	38
Risers		7	27-Jun-26	04-Jul-26	15-Apr-26 A	07-May-26 A	13,245.78	13,245.78	13,245.78	100%	100%	46
JDH4-02-007	Installation of Irrigation Riser with [Ro	7	27-Jun-26	04-Jul-26	15-Apr-26 A	07-May-26 A	13,245.78	13,245.78	13,245.78	100%	100%	46
Potable Network		80	02-May-26	25-Jul-26	09-Mar-26 A	09-May-26 A	199,289.73	199,289.73	199,289.73	100%	100%	63
Pipe Works		56	02-May-26	08-Jul-26	09-Mar-26 A	30-Apr-26 A	125,752.87	125,752.87	125,752.87	100%	100%	56
JDH4-02-007	Excavation and Compaction (FDT) [I	11	02-May-26	13-May-26	09-Mar-26 A	09-Apr-26 A	12,575.30	12,575.30	12,575.30	100%	100%	30

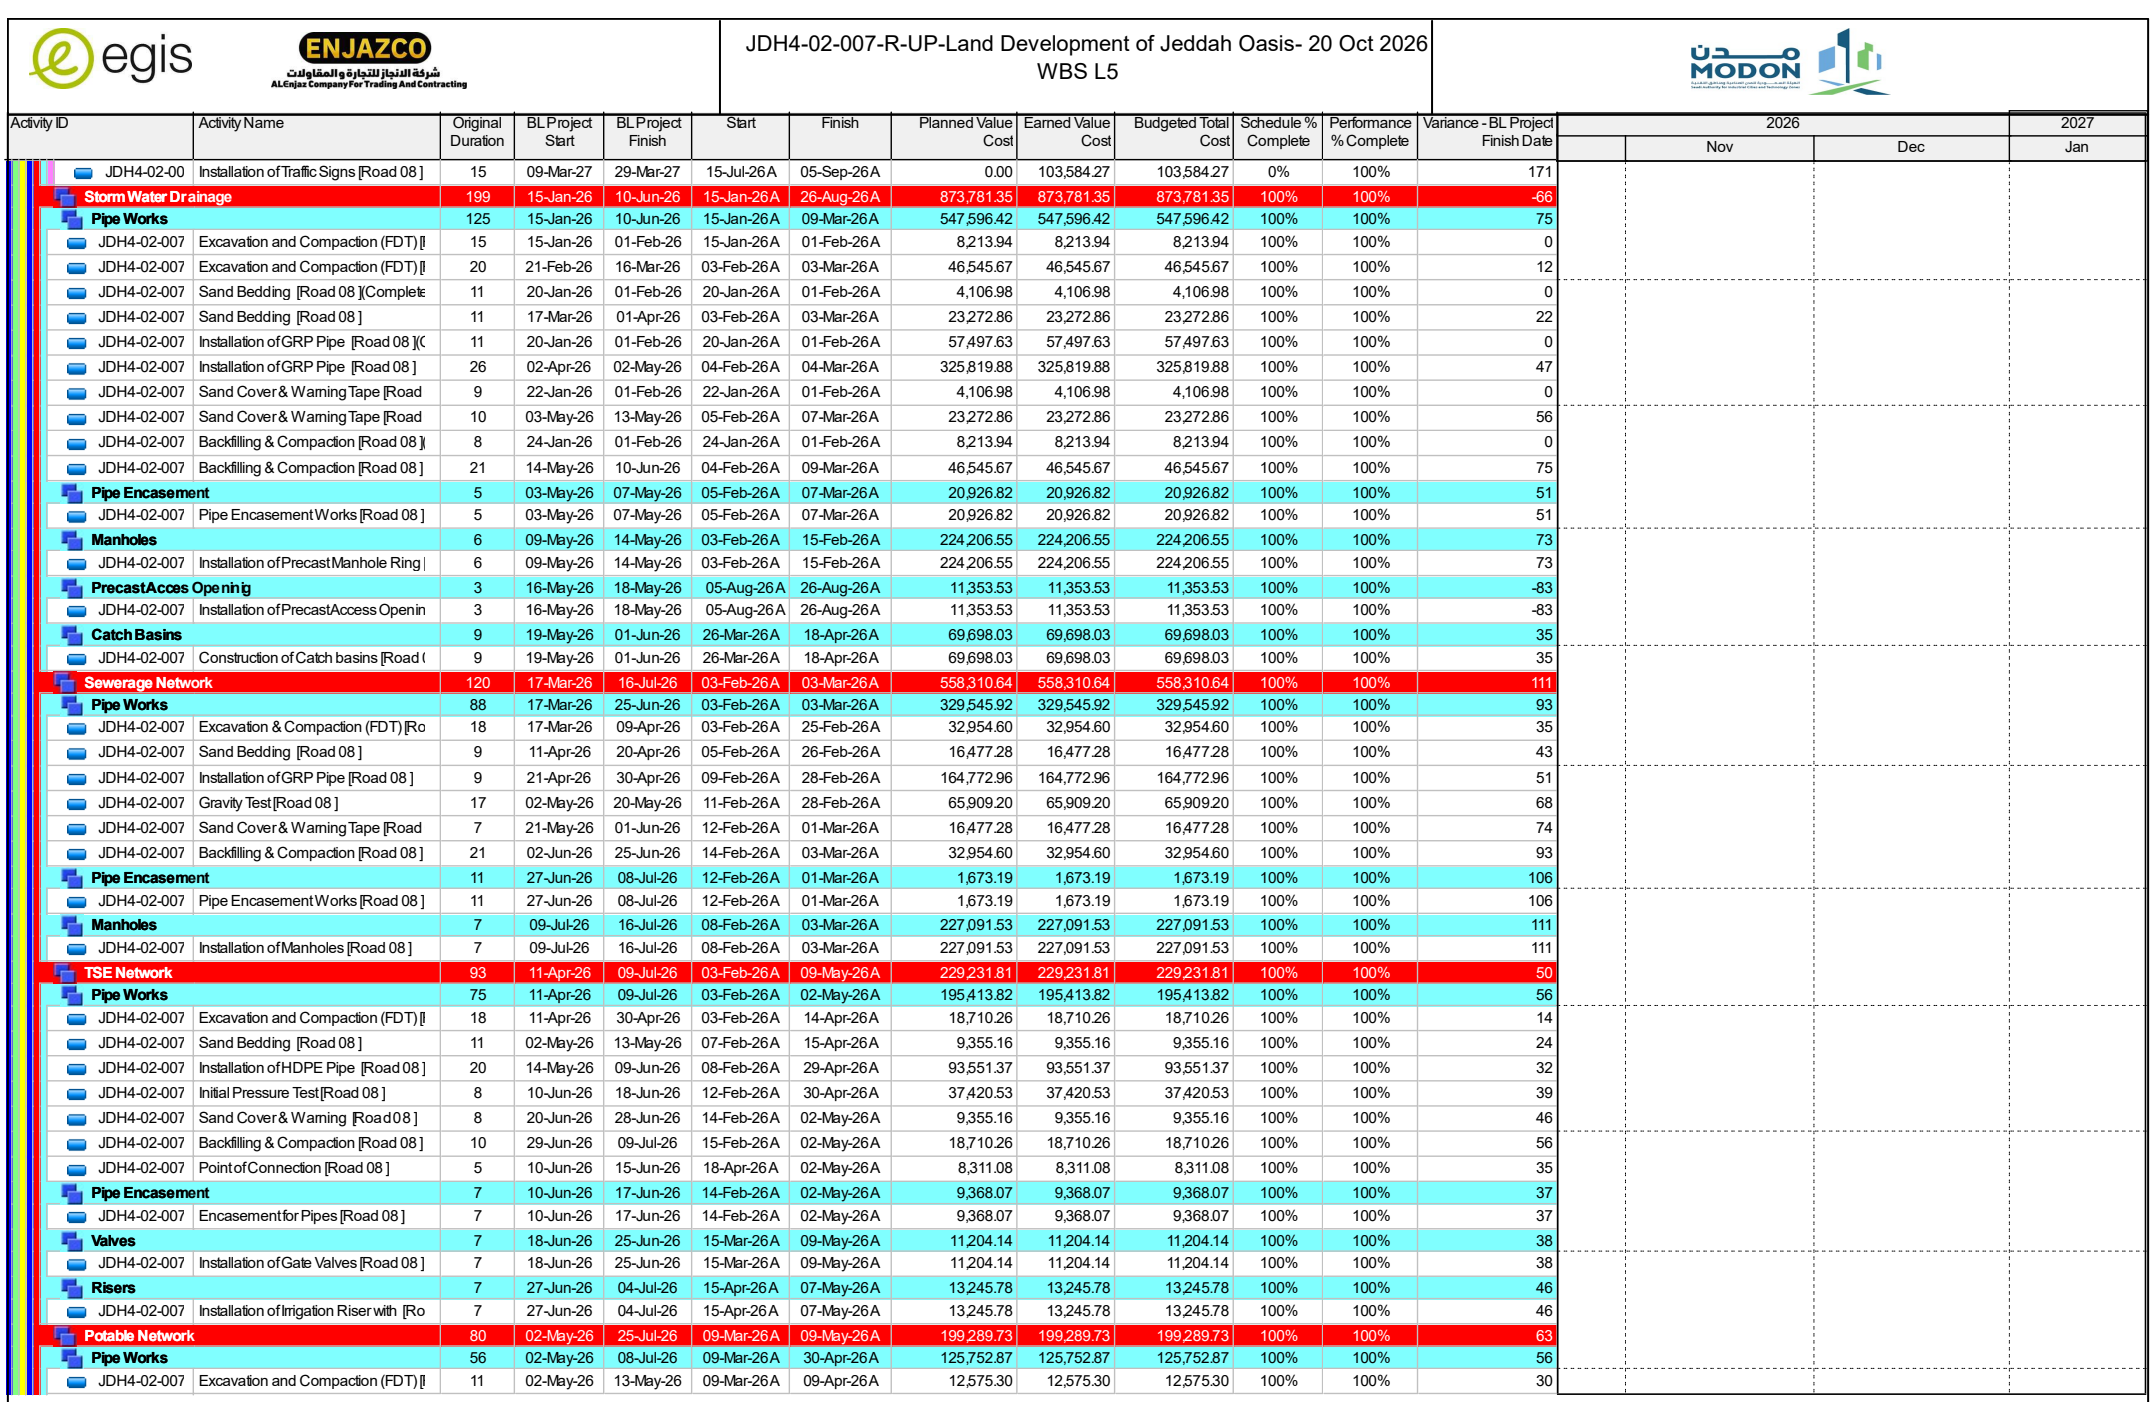


Date	Revision	Checked	Approved

Activity ID	Activity Name	Original Duration	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Schedule % Complete	Performance % Complete	Variance - BL Project Finish Date	2026 Nov / Dec	2027 Jan
JDH4-02-007	Sand Bedding [Road 08]	8	14-May-26	23-May-26	11-Mar-26 A	13-Apr-26 A	6,287.65	6,287.65	6,287.65	100%	100%	34		
JDH4-02-007	Installation of HDPE Pipe [Road 08]	15	24-May-26	13-Jun-26	14-Mar-26 A	29-Apr-26 A	62,876.41	62,876.41	62,876.41	100%	100%	35		
JDH4-02-007	Initial Pressure Test [Road 08]	6	14-Jun-26	20-Jun-26	17-Mar-26 A	30-Apr-26 A	25,150.56	25,150.56	25,150.56	100%	100%	40		
JDH4-02-007	Sand Cover & Warning Tape [Road	6	21-Jun-26	27-Jun-26	24-Mar-26 A	01-Apr-26 A	6,287.65	6,287.65	6,287.65	100%	100%	71		
JDH4-02-007	Backfilling [Road 08]	10	28-Jun-26	08-Jul-26	28-Mar-26 A	02-Apr-26 A	12,575.30	12,575.30	12,575.30	100%	100%	80		
Pipe Encasement		5	14-Jun-26	18-Jun-26	14-Mar-26 A	29-Apr-26 A	9,936.10	9,936.10	9,936.10	100%	100%	40		
JDH4-02-007	Encasement for Pipes [Road 08]	5	14-Jun-26	18-Jun-26	14-Mar-26 A	29-Apr-26 A	9,936.10	9,936.10	9,936.10	100%	100%	40		
Valves		6	20-Jun-26	25-Jun-26	10-Mar-26 A	07-May-26 A	13,140.65	13,140.65	13,140.65	100%	100%	39		
JDH4-02-007	Installation of Gate Valves [Road 08]	6	20-Jun-26	25-Jun-26	10-Mar-26 A	07-May-26 A	13,140.65	13,140.65	13,140.65	100%	100%	39		
Fire Hydrant		7	18-Jul-26	25-Jul-26	15-Apr-26 A	09-May-26 A	50,460.11	50,460.11	50,460.11	100%	100%	63		
JDH4-02-007	Installation of 3-outlet fire hydrant [Ro	7	18-Jul-26	25-Jul-26	15-Apr-26 A	09-May-26 A	50,460.11	50,460.11	50,460.11	100%	100%	63		
Electrical Works		111	27-Jun-26	07-Nov-26	02-Apr-26 A	03-Oct-26 A	632,653.69	645,200.42	645,200.42	98.06%	100%	30	ectrical Works	
LV Cables		52	27-Jun-26	17-Aug-26	25-Jun-26 A	20-Aug-26 A	195,304.10	195,304.10	195,304.10	100%	100%	-2		
Low Voltage Cable		52	27-Jun-26	17-Aug-26	25-Jun-26 A	20-Aug-26 A	195,304.10	195,304.10	195,304.10	100%	100%	-2		
JDH4-02-00	Excavation for Low Voltage Cable [R	18	27-Jun-26	16-Jul-26	21-Jul-26 A	18-Aug-26 A	10,823.69	10,823.69	10,823.69	100%	100%	-28		
JDH4-02-00	Installation of Low Voltage Cables [R	6	18-Jul-26	23-Jul-26	23-Jul-26 A	19-Aug-26 A	29,946.31	29,946.31	29,946.31	100%	100%	-23		
JDH4-02-00	Installation of Low Voltage Distributio	11	25-Jul-26	05-Aug-26	15-Aug-26 A	16-Aug-26 A	15,768.79	15,768.79	15,768.79	100%	100%	-9	, 5-50A, MCCB) [Road 08]	
JDH4-02-00	Installation of Unit Substation , 13.8/0	5	06-Aug-26	11-Aug-26	25-Jul-26 A	20-Aug-26 A	75,690.17	75,690.17	75,690.17	100%	100%	-7	[Road 08]	
JDH4-02-00	Installation of Ring Main Unit (RMU) 3	5	12-Aug-26	17-Aug-26	25-Jun-26 A	20-Aug-26 A	63,075.14	63,075.14	63,075.14	100%	100%	-2		
Street Lighting		93	18-Jul-26	07-Nov-26	02-Apr-26 A	03-Oct-26 A	162,808.74	175,355.47	175,355.47	92.84%	100%	30	eet Lighting	
JDH4-02-007	Excavation for Low Voltage Cable [R	13	18-Jul-26	01-Aug-26	16-May-26 A	17-Aug-26 A	8,325.92	8,325.92	8,325.92	100%	100%	-13		
JDH4-02-007	Installation of Road Crossing Ducts [I	12	02-Aug-26	15-Aug-26	02-Apr-26 A	23-Apr-26 A	17,695.84	17,695.84	17,695.84	100%	100%	94		
JDH4-02-007	Installation of Low Voltage Cables [R	21	16-Aug-26	08-Sep-26	15-Jun-26 A	20-Aug-26 A	42,386.49	42,386.49	42,386.49	100%	100%	17		
JDH4-02-007	Installation of Lighting Poles [Road 0	16	21-Sep-26	10-Oct-26	13-May-26 A	13-Aug-26 A	79,467.35	79,467.35	79,467.35	100%	100%	49		
JDH4-02-007	Installation of Lighting Luminaires [R	12	11-Oct-26	24-Oct-26	16-May-26 A	13-Aug-26 A	14,933.14	19,910.85	19,910.85	75%	100%	61		
JDH4-02-007	Installation of Earthing System [Road	12	25-Oct-26	07-Nov-26	15-Aug-26 A	03-Oct-26 A	0.00	7,569.02	7,569.02	0%	100%	30	arthing System [Road 08]	
Telecommunication		38	02-Aug-26	22-Sep-26	02-Apr-26 A	18-Jun-26 A	274,540.85	274,540.85	274,540.85	100%	100%	82		
JDH4-02-007	Installation Road Crossing R/F 6 way	10	02-Aug-26	12-Aug-26	02-Apr-26 A	23-Apr-26 A	126,781.03	126,781.03	126,781.03	100%	100%	92		
JDH4-02-007	Installation Road Crossing Un R/F 6	10	13-Aug-26	24-Aug-26	05-Apr-26 A	22-Apr-26 A	3,973.73	3,973.73	3,973.73	100%	100%	103		
JDH4-02-007	Installation of 2 x 32 mm diameter HI	10	25-Aug-26	05-Sep-26	13-Jun-26 A	18-Jun-26 A	98,371.99	98,371.99	98,371.99	100%	100%	67		
JDH4-02-007	Installation of Manholes [Road 08]	15	06-Sep-26	22-Sep-26	16-Apr-26 A	18-May-26 A	45,414.10	45,414.10	45,414.10	100%	100%	106		
Road 07-N		376	04-Dec-25	15-Dec-26	04-Dec-25 A	06-Oct-26 A	4,821,463.68	5,511,432.43	5,511,432.43	87.48%	100%	61	Road 07-N	
Road Works		376	04-Dec-25	15-Dec-26	04-Dec-25 A	06-Oct-26 A	2,477,780.83	3,118,311.38	3,118,311.38	79.46%	100%	61	Road Works	
Earthworks & Site grading		159	04-Dec-25	06-Aug-26	04-Dec-25 A	09-May-26 A	1,345,959.82	1,345,959.82	1,345,959.82	100%	100%	74		
JDH4-02-007	Road excavation [Road 07-N](Com	51	04-Dec-25	01-Feb-26	04-Dec-25 A	01-Feb-26 A	13,629.33	13,629.33	13,629.33	100%	100%	0		
JDH4-02-007	Road excavation [Road 07-N]	24	21-Feb-26	24-Mar-26	17-Feb-26 A	04-Mar-26 A	16,658.08	16,658.08	16,658.08	100%	100%	14		
JDH4-02-007	Road backfilling [Road 07-N](Comp	45	11-Dec-25	01-Feb-26	11-Dec-25 A	01-Feb-26 A	418,403.53	418,403.53	418,403.53	100%	100%	0		
JDH4-02-007	Road backfilling [Road 07-N]	22	24-Feb-26	24-Mar-26	02-Feb-26 A	09-Mar-26 A	777,035.12	777,035.12	777,035.12	100%	100%	11		
JDH4-02-007	Subgrade [Road 07-N]	14	22-Jul-26	06-Aug-26	29-Apr-26 A	09-May-26 A	120,233.76	120,233.76	120,233.76	100%	100%	74		
Asphalt Works		25	08-Aug-26	22-Sep-26	07-May-26 A	31-May-26 A	805,652.45	805,652.45	805,652.45	100%	100%	98		
JDH4-02-007	Aggregate base course [Road 07-N	15	08-Aug-26	24-Aug-26	07-May-26 A	13-May-26 A	122,460.38	122,460.38	122,460.38	100%	100%	85		
JDH4-02-007	Prime Coat (MC1) [Road 07-N]	10	25-Aug-26	05-Sep-26	11-May-26 A	21-May-26 A	68,436.53	68,436.53	68,436.53	100%	100%	88		
JDH4-02-007	Bituminous base course [Road 07-N	15	06-Sep-26	22-Sep-26	17-May-26 A	31-May-26 A	614,755.54	614,755.54	614,755.54	100%	100%	98		
Finishing Works		115	24-Sep-26	15-Dec-26	24-May-26 A	06-Oct-26 A	326,168.55	966,699.11	966,699.11	33.74%	100%	61	Finishing Works	
Asphalt Wearing Course		24	24-Sep-26	21-Oct-26	09-Sep-26 A	10-Sep-26 A	326,168.55	362,429.75	362,429.75	89.99%	100%	35		
JDH4-02-00	Tack Coat (RC2) [Road 07-N]	15	24-Sep-26	11-Oct-26	09-Sep-26 A	10-Sep-26 A	36,078.98	36,078.98	36,078.98	100%	100%	26		
JDH4-02-00	Bituminous concrete wearing course	9	12-Oct-26	21-Oct-26	09-Sep-26 A	10-Sep-26 A	290,089.57	326,350.77	326,350.77	88.89%	100%	35	oad 07-N]	
Precast Concrete Curb		12	22-Oct-26	04-Nov-26	24-May-26 A	02-Jul-26 A	0.00	225,534.37	225,534.37	0%	100%	106		
JDH4-02-00	Installation of Precast Concrete curb	12	22-Oct-26	04-Nov-26	24-May-26 A	02-Jul-26 A	0.00	225,534.37	225,534.37	0%	100%	106		
Precast Interlocking block pavers		12	05-Nov-26	18-Nov-26	18-Jun-26 A	30-Jul-26 A	0.00	214,487.01	214,487.01	0%	100%	94		
JDH4-02-00	Installation of Interlocking block pave	12	05-Nov-26	18-Nov-26	18-Jun-26 A	30-Jul-26 A	0.00	214,487.01	214,487.01	0%	100%	94		

Date	Revision	Checked	Approved


Activity ID	Activity Name	Original Duration	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Schedule % Complete	Performance % Complete	Variance - BL Project Finish Date
Pavement Markings		7	24-Nov-26	01-Dec-26	24-Sep-26 A	27-Sep-26 A	0.00	60,663.71	60,663.71	0%	100%	56
JDH4-02-00	Pavement markings [Road 07-N]	7	24-Nov-26	01-Dec-26	24-Sep-26 A	27-Sep-26 A	0.00	60,663.71	60,663.71	0%	100%	56
Traffic Signage		12	02-Dec-26	15-Dec-26	15-Jul-26 A	06-Oct-26 A	0.00	103,584.27	103,584.27	0%	100%	61
JDH4-02-00	Installation of Traffic Signs [Road 07-N	12	02-Dec-26	15-Dec-26	15-Jul-26 A	06-Oct-26 A	0.00	103,584.27	103,584.27	0%	100%	61
Storm Water Drainage		160	25-Mar-26	08-Jul-26	02-Mar-26 A	23-Jul-26 A	936,796.60	936,796.60	936,796.60	100%	100%	-13
Pipe Works		72	25-Mar-26	27-Jun-26	02-Mar-26 A	28-Mar-26 A	649,331.81	649,331.81	649,331.81	100%	100%	75
JDH4-02-007	Excavation and Compaction (FDT) [I	24	25-Mar-26	21-Apr-26	02-Mar-26 A	16-Mar-26 A	64,933.15	64,933.15	64,933.15	100%	100%	28
JDH4-02-007	Sand Bedding [Road 07-N]	15	22-Apr-26	09-May-26	07-Mar-26 A	16-Mar-26 A	32,466.61	32,466.61	32,466.61	100%	100%	43
JDH4-02-007	Installation of GRP Pipe [Road 07-N	16	10-May-26	31-May-26	08-Mar-26 A	17-Mar-26 A	454,532.29	454,532.29	454,532.29	100%	100%	58
JDH4-02-007	Sand Cover & Warning Tape [Road	12	01-Jun-26	14-Jun-26	09-Mar-26 A	25-Mar-26 A	32,466.61	32,466.61	32,466.61	100%	100%	66
JDH4-02-007	Backfilling & Compaction [Road 07-N	11	15-Jun-26	27-Jun-26	09-Mar-26 A	28-Mar-26 A	64,933.15	64,933.15	64,933.15	100%	100%	75
Pipe Encasement		10	01-Jun-26	11-Jun-26	09-Mar-26 A	25-Mar-26 A	24,850.59	24,850.59	24,850.59	100%	100%	64
JDH4-02-007	Pipe Encasement Works [Road 07-I	10	01-Jun-26	11-Jun-26	09-Mar-26 A	25-Mar-26 A	24,850.59	24,850.59	24,850.59	100%	100%	64
Manholes		7	01-Jun-26	08-Jun-26	05-Mar-26 A	28-Mar-26 A	130,787.16	130,787.16	130,787.16	100%	100%	59
JDH4-02-007	Installation of Precast Manhole Ring [	7	01-Jun-26	08-Jun-26	05-Mar-26 A	28-Mar-26 A	130,787.16	130,787.16	130,787.16	100%	100%	59
Precast Access Opening		3	09-Jun-26	11-Jun-26	01-Jul-26 A	23-Jul-26 A	7,569.02	7,569.02	7,569.02	100%	100%	-36
JDH4-02-007	Installation of Precast Access Openin	3	09-Jun-26	11-Jun-26	01-Jul-26 A	23-Jul-26 A	7,569.02	7,569.02	7,569.02	100%	100%	-36
Catch Basins		10	13-Jun-26	23-Jun-26	12-Apr-26 A	02-May-26 A	73,797.91	73,797.91	73,797.91	100%	100%	42
JDH4-02-007	Construction of Catch basins [Road (	10	13-Jun-26	23-Jun-26	12-Apr-26 A	02-May-26 A	73,797.91	73,797.91	73,797.91	100%	100%	42
Concrete Outfalls		10	28-Jun-26	08-Jul-26	21-May-26 A	08-Jul-26 A	50,460.11	50,460.11	50,460.11	100%	100%	0
JDH4-02-007	Construction of Concrete outfall struc	10	28-Jun-26	08-Jul-26	21-May-26 A	08-Jul-26 A	50,460.11	50,460.11	50,460.11	100%	100%	0
Sewerage Network		67	22-Apr-26	06-Jul-26	02-Mar-26 A	28-Mar-26 A	489,984.35	489,984.35	489,984.35	100%	100%	83
Pipe Works		56	22-Apr-26	06-Jul-26	02-Mar-26 A	26-Mar-26 A	326,102.92	326,102.92	326,102.92	100%	100%	84
JDH4-02-007	Excavation & Compaction (FDT) [Ro	21	22-Apr-26	16-May-26	02-Mar-26 A	15-Mar-26 A	32,610.30	32,610.30	32,610.30	100%	100%	50
JDH4-02-007	Sand Bedding [Road 07-N]	9	17-May-26	30-May-26	04-Mar-26 A	16-Mar-26 A	16,305.13	16,305.13	16,305.13	100%	100%	58
JDH4-02-007	Installation of GRP Pipe [Road 07-N	12	31-May-26	13-Jun-26	07-Mar-26 A	17-Mar-26 A	163,051.46	163,051.46	163,051.46	100%	100%	69
JDH4-02-007	Gravity Test [Road 07-N]	5	14-Jun-26	18-Jun-26	09-Mar-26 A	24-Mar-26 A	65,220.60	65,220.60	65,220.60	100%	100%	71
JDH4-02-007	Sand Cover & Warning Tape [Road	7	20-Jun-26	27-Jun-26	09-Mar-26 A	25-Mar-26 A	16,305.13	16,305.13	16,305.13	100%	100%	77
JDH4-02-007	Backfilling & Compaction [Road 07-N	8	28-Jun-26	06-Jul-26	09-Mar-26 A	26-Mar-26 A	32,610.30	32,610.30	32,610.30	100%	100%	84
Pipe Encasement		5	14-Jun-26	18-Jun-26	09-Mar-26 A	25-Mar-26 A	1,673.19	1,673.19	1,673.19	100%	100%	70
JDH4-02-007	Pipe Encasement Works [Road 07-I	5	14-Jun-26	18-Jun-26	09-Mar-26 A	25-Mar-26 A	1,673.19	1,673.19	1,673.19	100%	100%	70
Manholes		7	20-Jun-26	27-Jun-26	04-Mar-26 A	28-Mar-26 A	162,208.24	162,208.24	162,208.24	100%	100%	75
JDH4-02-007	Installation of Manholes [Road 07-N	7	20-Jun-26	27-Jun-26	04-Mar-26 A	28-Mar-26 A	162,208.24	162,208.24	162,208.24	100%	100%	75
TSE Network		211	17-May-26	25-Nov-26	03-Mar-26 A	09-May-26 A	223,897.62	244,612.82	244,612.82	91.53%	100%	168
Pipe Works		156	17-May-26	25-Aug-26	03-Mar-26 A	31-Mar-26 A	214,076.25	214,076.25	214,076.25	100%	100%	123
JDH4-02-007	Excavation and Compaction (FDT) [I	15	17-May-26	06-Jun-26	03-Mar-26 A	07-Mar-26 A	20,576.51	20,576.51	20,576.51	100%	100%	72
JDH4-02-007	Sand Bedding [Road 07-N]	12	07-Jun-26	20-Jun-26	08-Mar-26 A	10-Mar-26 A	10,288.28	10,288.28	10,288.28	100%	100%	81
JDH4-02-007	Installation of HDPE Pipe [Road 07-	15	21-Jun-26	07-Jul-26	11-Mar-26 A	28-Mar-26 A	102,882.58	102,882.58	102,882.58	100%	100%	84
JDH4-02-007	Initial Pressure Test [Road 07-N]	5	08-Jul-26	13-Jul-26	24-Mar-26 A	30-Mar-26 A	41,153.01	41,153.01	41,153.01	100%	100%	87
JDH4-02-007	Sand Cover & Warning [Road 07-N	7	14-Jul-26	21-Jul-26	28-Mar-26 A	30-Mar-26 A	10,288.28	10,288.28	10,288.28	100%	100%	94
JDH4-02-007	Backfilling & Compaction [Road 07-N	12	22-Jul-26	04-Aug-26	26-Mar-26 A	31-Mar-26 A	20,576.51	20,576.51	20,576.51	100%	100%	105
JDH4-02-007	Point of Connection [Road 07-N]	2	24-Aug-26	25-Aug-26	30-Mar-26 A	31-Mar-26 A	8,311.08	8,311.08	8,311.08	100%	100%	123
Pipe Encasement		4	08-Jul-26	12-Jul-26	28-Mar-26 A	30-Mar-26 A	9,821.37	9,821.37	9,821.37	100%	100%	86
JDH4-02-007	Encasement for Pipes [Road 07-N]	4	08-Jul-26	12-Jul-26	28-Mar-26 A	30-Mar-26 A	9,821.37	9,821.37	9,821.37	100%	100%	86
Valves		7	18-Nov-26	25-Nov-26	15-Apr-26 A	09-May-26 A	0.00	7,469.42	7,469.42	0%	100%	168
JDH4-02-007	Installation of Gate Valves [Road 07-I	7	18-Nov-26	25-Nov-26	15-Apr-26 A	09-May-26 A	0.00	7,469.42	7,469.42	0%	100%	168
Risers		5	18-Nov-26	23-Nov-26	24-Mar-26 A	30-Mar-26 A	0.00	13,245.78	13,245.78	0%	100%	201
JDH4-02-007	Installation of Irrigation Riser with [Ro	5	18-Nov-26	23-Nov-26	24-Mar-26 A	30-Mar-26 A	0.00	13,245.78	13,245.78	0%	100%	201
Potable Network		85	07-Jun-26	04-Aug-26	02-Mar-26 A	20-Apr-26 A	167,864.18	167,864.18	167,864.18	100%	100%	88
Pipe Works		51	07-Jun-26	04-Aug-26	02-Mar-26 A	31-Mar-26 A	98,143.31	98,143.31	98,143.31	100%	100%	105
JDH4-02-007	Excavation and Compaction (FDT) [I	9	07-Jun-26	16-Jun-26	02-Mar-26 A	08-Mar-26 A	9,814.34	9,814.34	9,814.34	100%	100%	80

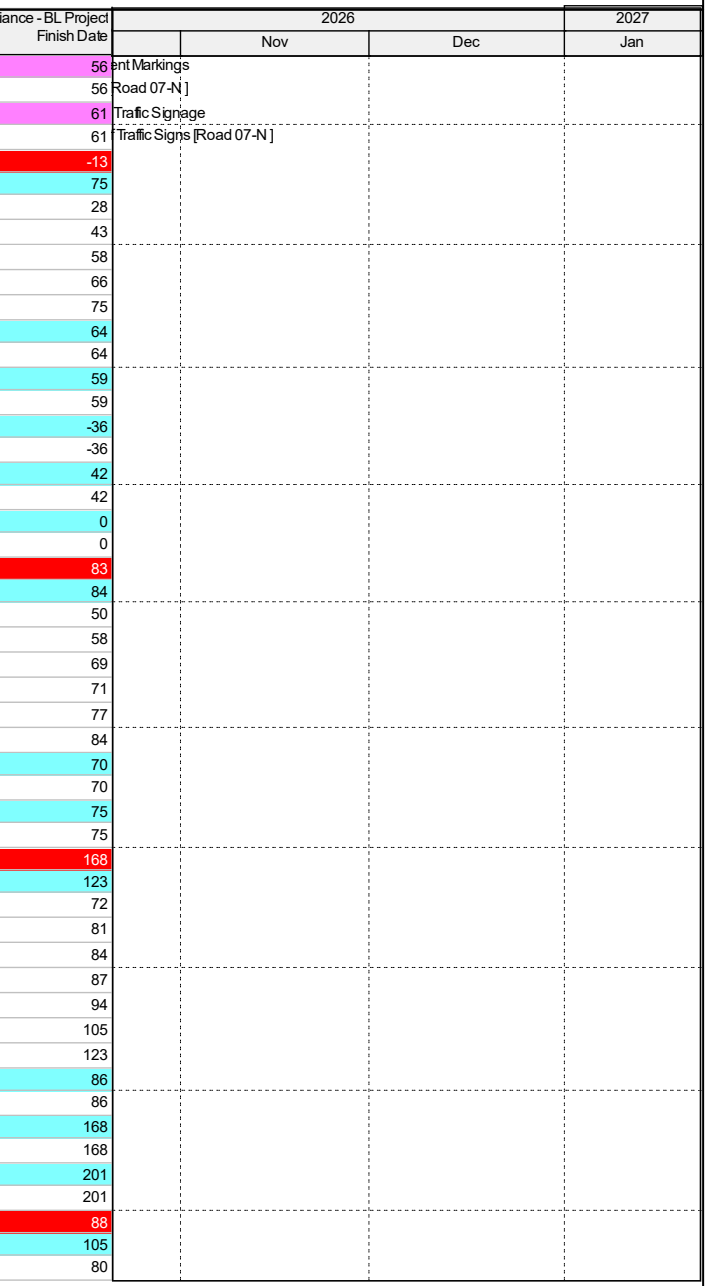

Actual Work
Remaining Work
Critical Remaining Work
Milestone

Date	Revision	Checked	Approved

Activity ID	Activity Name	Original Duration	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Schedule % Complete	Performance % Complete	Variance - BL Project Finish Date
JDH4-02-007	Sand Bedding [Road 07-N]	7	17-Jun-26	24-Jun-26	04-Mar-26 A	11-Mar-26 A	4,907.17	4,907.17	4,907.17	100%	100%	84
JDH4-02-007	Installation of HDPE Pipe [Road 07-	12	25-Jun-26	08-Jul-26	11-Mar-26 A	26-Mar-26 A	49,071.64	49,071.64	49,071.64	100%	100%	86
JDH4-02-007	Initial Pressure Test [Road 07-N]	5	09-Jul-26	14-Jul-26	25-Mar-26 A	26-Mar-26 A	19,628.65	19,628.65	19,628.65	100%	100%	91
JDH4-02-007	Sand Cover & Warning Tape [Road	6	15-Jul-26	21-Jul-26	25-Mar-26 A	28-Mar-26 A	4,907.17	4,907.17	4,907.17	100%	100%	96
JDH4-02-007	Backfilling [Road 07-N]	12	22-Jul-26	04-Aug-26	25-Mar-26 A	31-Mar-26 A	9,814.34	9,814.34	9,814.34	100%	100%	105
Pipe Encasement		5	09-Jul-26	14-Jul-26	25-Mar-26 A	28-Mar-26 A	7,696.98	7,696.98	7,696.98	100%	100%	90
JDH4-02-007	Encasement for Pipes [Road 07-N]	5	09-Jul-26	14-Jul-26	25-Mar-26 A	28-Mar-26 A	7,696.98	7,696.98	7,696.98	100%	100%	90
Valves		7	09-Jul-26	16-Jul-26	10-Mar-26 A	26-Mar-26 A	5,256.26	5,256.26	5,256.26	100%	100%	93
JDH4-02-007	Installation of Gate Valves [Road 07-I	7	09-Jul-26	16-Jul-26	10-Mar-26 A	26-Mar-26 A	5,256.26	5,256.26	5,256.26	100%	100%	93
Fire Hydrant		7	18-Jul-26	25-Jul-26	15-Apr-26 A	20-Apr-26 A	56,767.63	56,767.63	56,767.63	100%	100%	79
JDH4-02-007	Installation of 3-outlet fire hydrant [Ro	7	18-Jul-26	25-Jul-26	15-Apr-26 A	20-Apr-26 A	56,767.63	56,767.63	56,767.63	100%	100%	79
Electrical Works		171	07-Jun-26	09-Nov-26	12-Apr-26 A	03-Oct-26 A	525,140.11	553,863.10	553,863.10	94.81%	100%	32
LV Cables		18	07-Jun-26	27-Jun-26	15-Jul-26 A	06-Aug-26 A	35,076.36	35,076.36	35,076.36	100%	100%	-35
Low Voltage Cable		18	07-Jun-26	27-Jun-26	15-Jul-26 A	06-Aug-26 A	35,076.36	35,076.36	35,076.36	100%	100%	-35
JDH4-02-00	Excavation for Low Voltage Cable [R	10	07-Jun-26	17-Jun-26	15-Jul-26 A	05-Aug-26 A	9,385.58	9,385.58	9,385.58	100%	100%	-42
JDH4-02-00	Installation of Low Voltage Cables [R	8	18-Jun-26	27-Jun-26	18-Jul-26 A	06-Aug-26 A	25,690.78	25,690.78	25,690.78	100%	100%	-35
Street Lighting		171	18-Jun-26	09-Nov-26	16-Apr-26 A	03-Oct-26 A	238,860.70	267,583.69	267,583.69	89.27%	100%	32
JDH4-02-007	Excavation for Low Voltage Cable [R	13	18-Jun-26	02-Jul-26	18-Jun-26 A	08-Aug-26 A	17,282.59	17,282.59	17,282.59	100%	100%	-30
JDH4-02-007	Installation of Road Crossing Ducts [I	12	04-Jul-26	16-Jul-26	16-Apr-26 A	23-Apr-26 A	17,204.29	17,204.29	17,204.29	100%	100%	69
JDH4-02-007	Installation of Low Voltage Cables [R	18	18-Jul-26	06-Aug-26	20-Jun-26 A	10-Aug-26 A	88,141.20	88,141.20	88,141.20	100%	100%	-2
JDH4-02-007	Installation of Lighting Poles [Road 0	16	24-Sep-26	12-Oct-26	10-Jun-26 A	23-Jul-26 A	96,197.32	96,197.32	96,197.32	100%	100%	68
JDH4-02-007	Installation of Lighting Luminaires [R	8	13-Oct-26	21-Oct-26	09-Jun-26 A	23-Jul-26 A	20,035.29	22,897.48	22,897.48	87.5%	100%	76
JDH4-02-007	Installation of Street Lighting Feeder	8	22-Oct-26	31-Oct-26	30-Jun-26 A	03-Oct-26 A	0.00	22,076.30	22,076.30	0%	100%	25
JDH4-02-007	Installation of Earthing System [Road	8	01-Nov-26	09-Nov-26	17-Sep-26 A	03-Oct-26 A	0.00	3,784.51	3,784.51	0%	100%	32
Telecommunication		81	04-Jul-26	27-Aug-26	12-Apr-26 A	10-Aug-26 A	251,203.05	251,203.05	251,203.05	100%	100%	16
JDH4-02-007	Installation Road Crossing R/F 6 way	12	04-Jul-26	16-Jul-26	12-Apr-26 A	16-Jul-26 A	145,325.12	145,325.12	145,325.12	100%	100%	0
JDH4-02-007	Installation Road Crossing Un R/F 6	12	18-Jul-26	30-Jul-26	16-Apr-26 A	06-May-26 A	3,973.73	3,973.73	3,973.73	100%	100%	70
JDH4-02-007	Installation of 2 x 32 mm diameter HI	12	01-Aug-26	13-Aug-26	08-Aug-26 A	10-Aug-26 A	62,166.86	62,166.86	62,166.86	100%	100%	4
JDH4-02-007	Installation of Manholes [Road 07-N]	12	15-Aug-26	27-Aug-26	28-May-26 A	03-Jun-26 A	39,737.34	39,737.34	39,737.34	100%	100%	73
Road 01		292	07-Jan-26	23-Nov-26	07-Jan-26 A	03-Nov-26	3,230,122.96	3,382,506.18	3,400,633.43	94.99%	99.47%	17
Road Works (Roundabout)		137	03-Feb-26	23-Nov-26	15-Jul-26 A	03-Nov-26	656,188.53	808,571.75	826,699.00	79.37%	97.81%	17
Eartworks & Site grading		106	03-Feb-26	27-Jul-26	15-Jul-26 A	28-Jul-26 A	357,790.57	357,790.57	357,790.57	100%	100%	-1
JDH4-02-007	Road excavation [Road 01]	10	03-Feb-26	14-Feb-26	15-Jul-26 A	19-Jul-26 A	8,053.45	8,053.45	8,053.45	100%	100%	-126
JDH4-02-007	Road backfilling [Road 01]	7	15-Feb-26	23-Feb-26	20-Jul-26 A	23-Jul-26 A	317,788.32	317,788.32	317,788.32	100%	100%	-123
JDH4-02-007	Subgrade [Road 01]	7	20-Jul-26	27-Jul-26	25-Jul-26 A	28-Jul-26 A	31,948.80	31,948.80	31,948.80	100%	100%	-1
Asphalt Works		31	28-Jul-26	22-Sep-26	29-Jul-26 A	30-Aug-26 A	213,995.02	213,995.02	213,995.02	100%	100%	20
JDH4-02-007	Aggregate base course [Road 01]	10	28-Jul-26	08-Aug-26	29-Jul-26 A	21-Aug-26 A	32,540.46	32,540.46	32,540.46	100%	100%	-11
JDH4-02-007	Prime Coat (MC1) [Road 01]	21	09-Aug-26	01-Sep-26	02-Aug-26 A	29-Aug-26 A	17,989.03	17,989.03	17,989.03	100%	100%	3
JDH4-02-007	Bituminous base course [Road 01]	18	02-Sep-26	22-Sep-26	04-Aug-26 A	30-Aug-26 A	163,465.53	163,465.53	163,465.53	100%	100%	20
Finishing Works		37	24-Sep-26	23-Nov-26	23-Sep-26 A	03-Nov-26	84,402.94	236,786.16	254,913.41	33.11%	92.89%	17
Asphalt Wearing Course		25	24-Sep-26	22-Oct-26	07-Oct-26 A	12-Oct-26 A	84,402.94	95,937.28	95,937.28	87.98%	100%	9
JDH4-02-00	Tack Coat (RC2) [Road 01]	10	24-Sep-26	05-Oct-26	07-Oct-26 A	08-Oct-26 A	9,429.73	9,429.73	9,429.73	100%	100%	-3
JDH4-02-00	Bituminous concrete wearing course	15	06-Oct-26	22-Oct-26	08-Oct-26 A	12-Oct-26 A	74,973.21	86,507.55	86,507.55	86.67%	100%	9
Precast Concrete Curb		8	24-Oct-26	01-Nov-26	23-Sep-26 A	06-Oct-26 A	0.00	59,926.12	59,926.12	0%	100%	22
JDH4-02-00	Installation of Precast Concrete curb	8	24-Oct-26	01-Nov-26	23-Sep-26 A	06-Oct-26 A	0.00	59,926.12	59,926.12	0%	100%	22
Precast Interlocking block pavers		4	02-Nov-26	05-Nov-26	23-Sep-26 A	24-Sep-26 A	0.00	57,004.16	57,004.16	0%	100%	36
JDH4-02-00	Installation of Interlocking block pave	4	02-Nov-26	05-Nov-26	23-Sep-26 A	24-Sep-26 A	0.00	57,004.16	57,004.16	0%	100%	36
Pavement Markings		4	05-Nov-26	09-Nov-26	17-Oct-26 A	19-Oct-26 A	0.00	16,149.78	16,149.78	0%	100%	18
JDH4-02-00	Pavement markings [Road 01]	4	05-Nov-26	09-Nov-26	17-Oct-26 A	19-Oct-26 A	0.00	16,149.78	16,149.78	0%	100%	18
Traffic Signage		12	10-Nov-26	23-Nov-26	19-Oct-26 A	03-Nov-26	0.00	7,768.82	25,896.07	0%	30%	17
JDH4-02-00	Installation of Traffic Signs [Road 01]	12	10-Nov-26	23-Nov-26	19-Oct-26 A	03-Nov-26	0.00	7,768.82	25,896.07	0%	30%	17

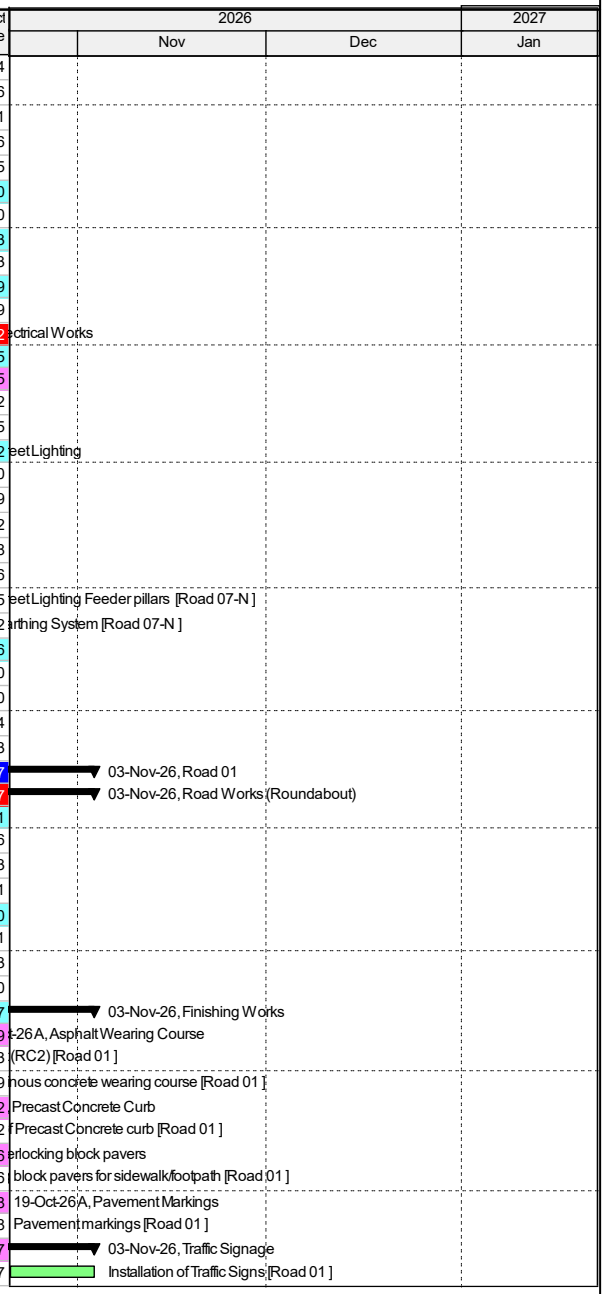

Date	Revision	Checked	Approved


Activity ID	Activity Name	Original Duration	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Schedule % Complete	Performance % Complete	Variance - BL Project Finish Date
Storm Water Drainage		77	24-Feb-26	22-Apr-26	13-May-26 A	26-Aug-26 A	131,305.17	131,305.17	131,305.17	100%	100%	-105
Pipe Works		34	24-Feb-26	07-Apr-26	13-May-26 A	18-Jun-26 A	26,247.15	26,247.15	26,247.15	100%	100%	-59
JDH4-02-007	Excavation and Compaction (FDT) [I	12	24-Feb-26	09-Mar-26	13-May-26 A	01-Jun-26 A	2,624.71	2,624.71	2,624.71	100%	100%	-65
JDH4-02-007	Sand Bedding [Road 01]	6	10-Mar-26	16-Mar-26	16-May-26 A	02-Jun-26 A	1,312.36	1,312.36	1,312.36	100%	100%	-61
JDH4-02-007	Installation of GRP Pipe [Road 01]	5	17-Mar-26	25-Mar-26	21-May-26 A	04-Jun-26 A	18,373.01	18,373.01	18,373.01	100%	100%	-58
JDH4-02-007	Sand Cover & Warning Tape [Road	6	26-Mar-26	01-Apr-26	23-May-26 A	17-Jun-26 A	1,312.36	1,312.36	1,312.36	100%	100%	-63
JDH4-02-007	Backfilling & Compaction [Road 01]	5	02-Apr-26	07-Apr-26	24-May-26 A	18-Jun-26 A	2,624.71	2,624.71	2,624.71	100%	100%	-59
Pipe Encasement		4	26-Mar-26	30-Mar-26	23-May-26 A	17-Jun-26 A	1,307.93	1,307.93	1,307.93	100%	100%	-65
JDH4-02-007	Pipe Encasement Works [Road 01]	4	26-Mar-26	30-Mar-26	23-May-26 A	17-Jun-26 A	1,307.93	1,307.93	1,307.93	100%	100%	-65
Manholes		6	31-Mar-26	06-Apr-26	16-May-26 A	13-Jun-26 A	74,735.52	74,735.52	74,735.52	100%	100%	-55
JDH4-02-007	Installation of Precast Manhole Ring	6	31-Mar-26	06-Apr-26	16-May-26 A	13-Jun-26 A	74,735.52	74,735.52	74,735.52	100%	100%	-55
PrecastAcces Openi g		6	07-Apr-26	13-Apr-26	05-Aug-26 A	26-Aug-26 A	3,784.51	3,784.51	3,784.51	100%	100%	-113
JDH4-02-007	Installation of PrecastAccess Openin	6	07-Apr-26	13-Apr-26	05-Aug-26 A	26-Aug-26 A	3,784.51	3,784.51	3,784.51	100%	100%	-113
Concrete Outfalls		8	14-Apr-26	22-Apr-26	06-Aug-26 A	09-Aug-26 A	25,230.06	25,230.06	25,230.06	100%	100%	-90
JDH4-02-007	Construction of Concrete outfall struc	8	14-Apr-26	22-Apr-26	06-Aug-26 A	09-Aug-26 A	25,230.06	25,230.06	25,230.06	100%	100%	-90
Sewerage Network		45	10-Mar-26	04-May-26	10-May-26 A	29-Jun-26 A	134,037.33	134,037.33	134,037.33	100%	100%	-45
Pipe Works		45	10-Mar-26	04-May-26	20-May-26 A	18-Jun-26 A	52,628.99	52,628.99	52,628.99	100%	100%	-36
JDH4-02-007	Excavation & Compaction (FDT) [Ro	10	10-Mar-26	24-Mar-26	20-May-26 A	24-May-26 A	5,262.90	5,262.90	5,262.90	100%	100%	-52
JDH4-02-007	Sand Bedding [Road 01]	10	25-Mar-26	05-Apr-26	25-May-26 A	28-May-26 A	2,631.45	2,631.45	2,631.45	100%	100%	-43
JDH4-02-007	Installation of GRP Pipe [Road 01]	12	06-Apr-26	19-Apr-26	30-May-26 A	04-Jun-26 A	26,314.49	26,314.49	26,314.49	100%	100%	-37
JDH4-02-007	Gravity Test [Road 01]	3	20-Apr-26	22-Apr-26	06-Jun-26 A	08-Jun-26 A	10,525.80	10,525.80	10,525.80	100%	100%	-37
JDH4-02-007	Sand Cover & Warning Tape [Road	4	23-Apr-26	27-Apr-26	09-Jun-26 A	13-Jun-26 A	2,631.45	2,631.45	2,631.45	100%	100%	-37
JDH4-02-007	Backfilling & Compaction [Road 01]	6	28-Apr-26	04-May-26	13-Jun-26 A	18-Jun-26 A	5,262.90	5,262.90	5,262.90	100%	100%	-36
Pipe Encasement		4	20-Apr-26	23-Apr-26	28-May-26 A	24-Jun-26 A	304.22	304.22	304.22	100%	100%	-50
JDH4-02-007	Pipe Encasement Works [Road 01]	4	20-Apr-26	23-Apr-26	28-May-26 A	24-Jun-26 A	304.22	304.22	304.22	100%	100%	-50
Manholes		6	25-Apr-26	30-Apr-26	10-May-26 A	29-Jun-26 A	81,104.12	81,104.12	81,104.12	100%	100%	-48
JDH4-02-007	Installation of Manholes [Road 01]	6	25-Apr-26	30-Apr-26	10-May-26 A	29-Jun-26 A	81,104.12	81,104.12	81,104.12	100%	100%	-48
TSE Network		175	07-Jan-26	04-Jun-26	07-Jan-26 A	02-Jul-26 A	315,346.48	315,346.48	315,346.48	100%	100%	-24
Pipe Works		175	07-Jan-26	04-Jun-26	07-Jan-26 A	30-Jun-26 A	199,841.72	199,841.72	199,841.72	100%	100%	-22
JDH4-02-007	Excavation and Compaction (FDT) [I	22	07-Jan-26	01-Feb-26	07-Jan-26 A	01-Feb-26 A	4,579.90	4,579.90	4,579.90	100%	100%	0
JDH4-02-007	Excavation and Compaction (FDT) [I	12	10-Mar-26	26-Mar-26	07-Feb-26 A	23-Mar-26 A	13,739.69	13,739.69	13,739.69	100%	100%	3
JDH4-02-007	Sand Bedding [Road 01](Complete	20	10-Jan-26	01-Feb-26	10-Jan-26 A	01-Feb-26 A	2,289.96	2,289.96	2,289.96	100%	100%	0
JDH4-02-007	Sand Bedding [Road 01]	11	28-Mar-26	08-Apr-26	10-Feb-26 A	26-Mar-26 A	6,869.87	6,869.87	6,869.87	100%	100%	11
JDH4-02-007	Installation of HDPE Pipe [Road 01]	21	08-Jan-26	01-Feb-26	08-Jan-26 A	01-Feb-26 A	22,899.50	22,899.50	22,899.50	100%	100%	0
JDH4-02-007	Installation of HDPE Pipe [Road 01]	12	09-Apr-26	22-Apr-26	12-Feb-26 A	25-Jun-26 A	68,698.50	68,698.50	68,698.50	100%	100%	-52
JDH4-02-007	Initial Pressure Test [Road 01]	10	23-Apr-26	04-May-26	15-Feb-26 A	27-Jun-26 A	36,654.89	36,654.89	36,654.89	100%	100%	-43
JDH4-02-007	Sand Cover & Warning [Road 01](C	14	17-Jan-26	01-Feb-26	17-Jan-26 A	01-Feb-26 A	2,106.76	2,106.76	2,106.76	100%	100%	0
JDH4-02-007	Sand Cover & Warning [Road 01]	8	05-May-26	13-May-26	16-Feb-26 A	29-Jun-26 A	7,053.06	7,053.06	7,053.06	100%	100%	-37
JDH4-02-007	Backfilling & Compaction [Road 01]	12	14-May-26	31-May-26	16-Feb-26 A	28-Jun-26 A	18,327.45	18,327.45	18,327.45	100%	100%	-24
JDH4-02-007	Point of Connection [Road 01]	4	01-Jun-26	04-Jun-26	18-Apr-26 A	30-Jun-26 A	16,622.15	16,622.15	16,622.15	100%	100%	-22
Pipe Encasement		3	23-Apr-26	26-Apr-26	16-Feb-26 A	29-Jun-26 A	9,065.88	9,065.88	9,065.88	100%	100%	-52
JDH4-02-007	Encasement for Pipes [Road 01]	3	23-Apr-26	26-Apr-26	16-Feb-26 A	29-Jun-26 A	9,065.88	9,065.88	9,065.88	100%	100%	-52
Valves		70	27-Apr-26	10-May-26	04-Mar-26 A	02-Jul-26 A	93,193.10	93,193.10	93,193.10	100%	100%	-43
JDH4-02-007	Installation of Gate Valves [Road 01]	3	27-Apr-26	29-Apr-26	04-Mar-26 A	06-May-26 A	11,204.14	11,204.14	11,204.14	100%	100%	-6
JDH4-02-007	Installation of Butterfly Valves [Road (	3	30-Apr-26	03-May-26	16-Apr-26 A	02-Jul-26 A	44,152.60	44,152.60	44,152.60	100%	100%	-49
JDH4-02-007	Installation of Washout Valves [Road	3	04-May-26	06-May-26	16-Apr-26 A	07-May-26 A	23,329.08	23,329.08	23,329.08	100%	100%	-1
JDH4-02-007	Installation of Air Valves [Road 01]	3	07-May-26	10-May-26	19-Apr-26 A	07-May-26 A	14,507.28	14,507.28	14,507.28	100%	100%	2
Risers		3	11-May-26	13-May-26	15-Apr-26 A	20-Apr-26 A	13,245.78	13,245.78	13,245.78	100%	100%	20
JDH4-02-007	Installation of Irrigation Riser with [Ro	3	11-May-26	13-May-26	15-Apr-26 A	20-Apr-26 A	13,245.78	13,245.78	13,245.78	100%	100%	20
Potable Network		117	06-Jun-26	27-Aug-26	03-Feb-26 A	30-Jun-26 A	1,242,732.96	1,242,732.96	1,242,732.96	100%	100%	50
Pipe Works		66	06-Jun-26	20-Aug-26	03-Feb-26 A	22-Jun-26 A	176,873.66	176,873.66	176,873.66	100%	100%	51

2026		2027
Nov	Dec	Jan

Actual Work | Critical Remaining Work | Remaining Work | Milestone


Date	Revision	Checked	Approved

Activity ID	Activity Name	Original Duration	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Schedule % Complete	Performance % Complete	Variance - BL Project Finish Date
JDH4-02-007	Excavation and Compaction (FDT) [I	12	06-Jun-26	18-Jun-26	03-Feb-26A	16-Apr-26A	17,687.38	17,687.38	17,687.38	100%	100%	51
JDH4-02-007	Sand Bedding [Road 01]	10	20-Jun-26	30-Jun-26	16-Feb-26A	18-Jun-26A	8,843.69	8,843.69	8,843.69	100%	100%	10
JDH4-02-007	Installation of HDPE Pipe [Road 01]	12	01-Jul-26	14-Jul-26	08-Feb-26A	20-Jun-26A	88,436.81	88,436.81	88,436.81	100%	100%	21
JDH4-02-007	Initial Pressure Test [Road 01]	9	15-Jul-26	25-Jul-26	10-Feb-26A	21-Jun-26A	35,374.71	35,374.71	35,374.71	100%	100%	29
JDH4-02-007	Sand Cover & Warning Tape [Road	13	26-Jul-26	09-Aug-26	11-Feb-26A	22-Jun-26A	8,843.69	8,843.69	8,843.69	100%	100%	41
JDH4-02-007	Backfilling [Road 01]	10	10-Aug-26	20-Aug-26	12-Feb-26A	22-Jun-26A	17,687.38	17,687.38	17,687.38	100%	100%	51
Pipe Encasement		2	15-Jul-26	16-Jul-26	11-Feb-26A	22-Jun-26A	13,294.79	13,294.79	13,294.79	100%	100%	21
JDH4-02-007	Encasement for Pipes [Road 01]	2	15-Jul-26	16-Jul-26	11-Feb-26A	22-Jun-26A	13,294.79	13,294.79	13,294.79	100%	100%	21
Valves		29	18-Jul-26	04-Aug-26	25-Mar-26A	20-Apr-26A	141,183.18	141,183.18	141,183.18	100%	100%	88
JDH4-02-007	Installation of Gate Valves [Road 01]	3	18-Jul-26	20-Jul-26	25-Mar-26A	08-Apr-26A	13,140.65	13,140.65	13,140.65	100%	100%	85
JDH4-02-007	Installation of Butterfly valves [Road (	2	21-Jul-26	22-Jul-26	09-Apr-26A	13-Apr-26A	37,845.08	37,845.08	37,845.08	100%	100%	83
JDH4-02-007	Installation of Washout valves [Roac	5	23-Jul-26	28-Jul-26	11-Apr-26A	16-Apr-26A	29,645.31	29,645.31	29,645.31	100%	100%	85
JDH4-02-007	Installation of Air valves [Road 01]	6	29-Jul-26	04-Aug-26	16-Apr-26A	20-Apr-26A	60,552.14	60,552.14	60,552.14	100%	100%	88
Fire Hydrant		6	22-Aug-26	27-Aug-26	30-Apr-26A	30-Jun-26A	75,690.17	75,690.17	75,690.17	100%	100%	50
JDH4-02-007	Installation of 3-outlet fire hydrant [Ro	6	22-Aug-26	27-Aug-26	30-Apr-26A	30-Jun-26A	75,690.17	75,690.17	75,690.17	100%	100%	50
Valve Chambers		49	20-Jun-26	10-Aug-26	18-Feb-26A	20-Apr-26A	829,383.65	829,383.65	829,383.65	100%	100%	93
JDH4-02-007	Construction of Valve Chambers [Ro	4	20-Jun-26	23-Jun-26	18-Feb-26A	15-Apr-26A	104,035.14	104,035.14	104,035.14	100%	100%	56
JDH4-02-007	Construction of Wash out Chambers	9	24-Jun-26	04-Jul-26	28-Feb-26A	16-Apr-26A	261,848.64	261,848.64	261,848.64	100%	100%	64
JDH4-02-007	Construction of Air Valve Chambers [	8	05-Jul-26	13-Jul-26	01-Mar-26A	18-Apr-26A	274,274.46	274,274.46	274,274.46	100%	100%	71
JDH4-02-007	Construction of Valve Chambers [Ro	8	14-Jul-26	22-Jul-26	04-Mar-26A	19-Apr-26A	75,690.16	75,690.16	75,690.16	100%	100%	78
JDH4-02-007	Construction of Wash Out Valve Cha	8	23-Jul-26	01-Aug-26	15-Apr-26A	19-Apr-26A	37,845.08	37,845.08	37,845.08	100%	100%	86
JDH4-02-007	Construction of Air Valve Chambers [	8	02-Aug-26	10-Aug-26	14-Apr-26A	20-Apr-26A	75,690.17	75,690.17	75,690.17	100%	100%	93
Road Crossings		5	15-Jul-26	20-Jul-26	18-Jun-26A	25-Jun-26A	6,307.51	6,307.51	6,307.51	100%	100%	21
JDH4-02-007	Installation of HDPE road croosing [F	5	15-Jul-26	20-Jul-26	18-Jun-26A	25-Jun-26A	6,307.51	6,307.51	6,307.51	100%	100%	21
Electrical Works		52	01-Jun-26	24-Aug-26	09-May-26A	03-Oct-26A	360,707.74	360,707.74	360,707.74	100%	100%	-33
LV Cables		23	01-Jun-26	27-Jun-26	04-Jul-26A	03-Oct-26A	71,867.75	71,867.75	71,867.75	100%	100%	-83
Low Voltage Cable		23	01-Jun-26	27-Jun-26	04-Jul-26A	03-Oct-26A	71,867.75	71,867.75	71,867.75	100%	100%	-83
JDH4-02-00	Excavation for Low Voltage Cable [R	15	01-Jun-26	17-Jun-26	04-Jul-26A	24-Sep-26A	19,225.30	19,225.30	19,225.30	100%	100%	-84
JDH4-02-00	Installation of Low Voltage Cables [R	8	18-Jun-26	27-Jun-26	12-Jul-26A	03-Oct-26A	52,642.45	52,642.45	52,642.45	100%	100%	-83
Street Lighting		25	18-Jun-26	19-Jul-26	20-Jul-26A	13-Aug-26A	20,045.28	20,045.28	20,045.28	100%	100%	-22
JDH4-02-007	Excavation for Low Voltage Cable [R	13	18-Jun-26	02-Jul-26	20-Jul-26A	13-Aug-26A	3,279.91	3,279.91	3,279.91	100%	100%	-36
JDH4-02-007	Installation of Low Voltage Cables [R	14	04-Jul-26	19-Jul-26	26-Jul-26A	13-Aug-26A	16,765.37	16,765.37	16,765.37	100%	100%	-22
Telecommunication		45	04-Jul-26	24-Aug-26	09-May-26A	19-Aug-26A	268,794.71	268,794.71	268,794.71	100%	100%	4
JDH4-02-007	Installation Road Crossing R/F 6 way	15	04-Jul-26	20-Jul-26	16-May-26A	16-Aug-26A	206,634.16	206,634.16	206,634.16	100%	100%	-22
JDH4-02-007	Installation Road Crossing Un R/F 6	15	21-Jul-26	06-Aug-26	09-May-26A	29-Jun-26A	5,392.92	5,392.92	5,392.92	100%	100%	33
JDH4-02-007	Installation of Manholes [Road 01]	15	08-Aug-26	24-Aug-26	09-May-26A	19-Aug-26A	56,767.63	56,767.63	56,767.63	100%	100%	4
Open Drain Channel		120	28-Jan-26	19-May-26	28-Jan-26A	09-Mar-26A	389,804.76	389,804.76	389,804.76	100%	100%	58
JDH4-02-007-	Channel excavation [Road 01](Con	4	28-Jan-26	01-Feb-26	28-Jan-26A	01-Feb-26A	65,850.60	65,850.60	65,850.60	100%	100%	0
JDH4-02-007-	Channel excavation [Road 01]	21	03-Feb-26	28-Feb-26	03-Feb-26A	08-Feb-26A	98,775.90	98,775.90	98,775.90	100%	100%	16
JDH4-02-007-	Backfill of the existing channel [Road	4	28-Jan-26	01-Feb-26	28-Jan-26A	01-Feb-26A	30,276.07	30,276.07	30,276.07	100%	100%	0
JDH4-02-007-	Backfill of the existing channel [Road	21	01-Mar-26	28-Mar-26	04-Feb-26A	26-Feb-26A	20,184.04	20,184.04	20,184.04	100%	100%	23
JDH4-02-007-	Compaction [Road 01]	24	29-Mar-26	25-Apr-26	02-Feb-26A	01-Mar-26A	18,922.54	18,922.54	18,922.54	100%	100%	44
JDH4-02-007-	Finished grouted riprap for side ditch	21	26-Apr-26	19-May-26	04-Mar-26A	09-Mar-26A	155,795.60	155,795.60	155,795.60	100%	100%	58
Road 02		316	07-Jan-26	19-Dec-26	07-Jan-26A	27-Jun-26A	563,077.68	658,204.00	658,204.00	85.55%	100%	149
Under Pass		206	09-Jul-26	17-Sep-26	02-Feb-26A	18-Jun-26A	112,526.05	112,526.05	112,526.05	100%	100%	78
JDH4-02-007-	Compacted structural backfill for clos	14	09-Jul-26	25-Jul-26	02-Feb-26A	25-Mar-26A	16,651.84	16,651.84	16,651.84	100%	100%	101
JDH4-02-007-	RC wall and the foundation at face of	21	25-Aug-26	17-Sep-26	08-Apr-26A	18-Jun-26A	95,874.21	95,874.21	95,874.21	100%	100%	78
Sewerage Network		115	29-Mar-26	22-Jul-26	11-Jun-26A	22-Jun-26A	89,801.58	89,801.58	89,801.58	100%	100%	26
Pipe Works		38	29-Mar-26	04-May-26	11-Jun-26A	22-Jun-26A	57,055.71	57,055.71	57,055.71	100%	100%	-39
JDH4-02-007	Excavation & Compaction (FDT) [Ro	12	29-Mar-26	11-Apr-26	11-Jun-26A	15-Jun-26A	5,705.57	5,705.57	5,705.57	100%	100%	-53
JDH4-02-007	Sand Bedding [Road 02]	10	12-Apr-26	22-Apr-26	13-Jun-26A	17-Jun-26A	2,852.78	2,852.78	2,852.78	100%	100%	-45

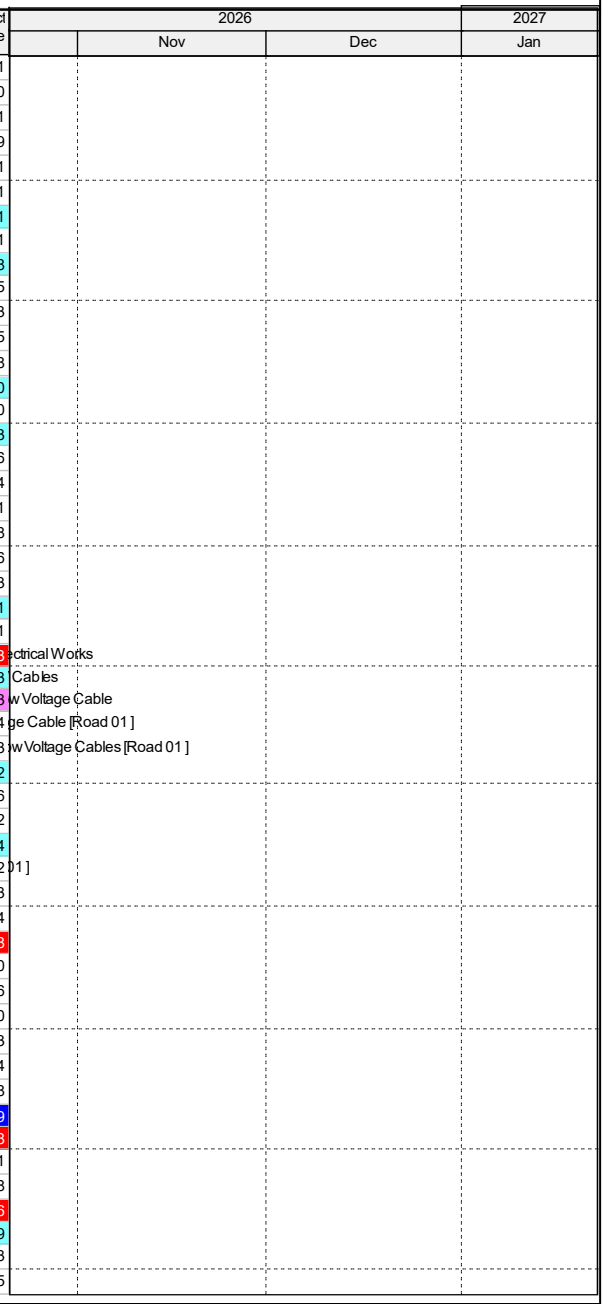


Date	Revision	Checked	Approved

Activity ID	Activity Name	Original Duration	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Schedule % Complete	Performance % Complete	Variance - BL Project Finish Date
JDH4-02-007	Installation of GRP Pipe [Road 02]	10	12-Apr-26	22-Apr-26	16-Jun-26 A	20-Jun-26 A	28,527.86	28,527.86	28,527.86	100%	100%	-47
JDH4-02-007	Gravity Test [Road 02]	3	23-Apr-26	26-Apr-26	21-Jun-26 A	22-Jun-26 A	11,411.15	11,411.15	11,411.15	100%	100%	-46
JDH4-02-007	Sand Cover & Warning Tape [Road	5	27-Apr-26	02-May-26	11-Jun-26 A	21-Jun-26 A	2,852.78	2,852.78	2,852.78	100%	100%	-40
JDH4-02-007	Backfilling & Compaction [Road 02]	7	27-Apr-26	04-May-26	22-Jun-26 A	22-Jun-26 A	5,705.57	5,705.57	5,705.57	100%	100%	-39
Pipe Encasement		7	23-Apr-26	30-Apr-26	11-Jun-26 A	21-Jun-26 A	304.22	304.22	304.22	100%	100%	-41
JDH4-02-007	Pipe Encasement Works [Road 02]	7	23-Apr-26	30-Apr-26	11-Jun-26 A	21-Jun-26 A	304.22	304.22	304.22	100%	100%	-41
Manholes		5	18-Jul-26	22-Jul-26	11-Jun-26 A	21-Jun-26 A	32,441.65	32,441.65	32,441.65	100%	100%	27
JDH4-02-007	Installation of Manholes [Road 02]	5	18-Jul-26	22-Jul-26	11-Jun-26 A	21-Jun-26 A	32,441.65	32,441.65	32,441.65	100%	100%	27
TSE Network		269	07-Jan-26	01-Oct-26	07-Jan-26 A	21-Jun-26 A	145,569.49	145,569.49	145,569.49	100%	100%	88
Pipe Works		240	07-Jan-26	23-Aug-26	07-Jan-26 A	21-Jun-26 A	112,992.76	112,992.76	112,992.76	100%	100%	55
JDH4-02-007	Excavation and Compaction (FDT) [I	22	07-Jan-26	01-Feb-26	07-Jan-26 A	01-Feb-26 A	5,754.78	5,754.78	5,754.78	100%	100%	0
JDH4-02-007	Excavation and Compaction (FDT) [I	18	20-May-26	13-Jun-26	28-Feb-26 A	01-Jun-26 A	4,708.46	4,708.46	4,708.46	100%	100%	10
JDH4-02-007	Sand Bedding [Road 02](Complete	20	10-Jan-26	01-Feb-26	10-Jan-26 A	01-Feb-26 A	2,877.40	2,877.40	2,877.40	100%	100%	0
JDH4-02-007	Sand Bedding [Road 02]	6	14-Jun-26	20-Jun-26	04-Mar-26 A	02-Jun-26 A	2,354.23	2,354.23	2,354.23	100%	100%	16
JDH4-02-007	Installation of HDPE Pipe [Road 02]	17	13-Jan-26	01-Feb-26	13-Jan-26 A	01-Feb-26 A	23,542.29	23,542.29	23,542.29	100%	100%	0
JDH4-02-007	Installation of HDPE Pipe [Road 02]	11	21-Jun-26	02-Jul-26	09-Mar-26 A	04-Jun-26 A	28,773.91	28,773.91	28,773.91	100%	100%	25
JDH4-02-007	Initial Pressure Test [Road 02]	5	04-Jul-26	08-Jul-26	14-Mar-26 A	06-Jun-26 A	20,959.32	20,959.32	20,959.32	100%	100%	29
JDH4-02-007	Sand Cover & Warning [Road 02](C	9	22-Jan-26	01-Feb-26	22-Jan-26 A	01-Feb-26 A	2,354.23	2,354.23	2,354.23	100%	100%	0
JDH4-02-007	Sand Cover & Warning [Road 02]	5	23-Jul-26	28-Jul-26	23-Mar-26 A	17-Jun-26 A	2,877.40	2,877.40	2,877.40	100%	100%	36
JDH4-02-007	Backfilling & Compaction [Road 02]	17	29-Jul-26	17-Aug-26	29-Mar-26 A	21-Jun-26 A	10,479.66	10,479.66	10,479.66	100%	100%	50
JDH4-02-007	Point of Connection [Road 02]	5	18-Aug-26	23-Aug-26	08-Apr-26 A	21-Jun-26 A	8,311.08	8,311.08	8,311.08	100%	100%	55
Pipe Encasement		10	26-Aug-26	06-Sep-26	23-Mar-26 A	17-Jun-26 A	5,288.43	5,288.43	5,288.43	100%	100%	70
JDH4-02-007	Encasement for Pipes [Road 02]	10	26-Aug-26	06-Sep-26	23-Mar-26 A	17-Jun-26 A	5,288.43	5,288.43	5,288.43	100%	100%	70
Valves		30	07-Sep-26	24-Sep-26	11-Mar-26 A	20-Apr-26 A	18,457.78	18,457.78	18,457.78	100%	100%	131
JDH4-02-007	Installation of Gate Valves [Road 02]	5	07-Sep-26	12-Sep-26	11-Mar-26 A	15-Apr-26 A	11,204.14	11,204.14	11,204.14	100%	100%	125
JDH4-02-007	Installation of Air Valves [Road 02]	5	19-Sep-26	24-Sep-26	15-Apr-26 A	20-Apr-26 A	7,253.64	7,253.64	7,253.64	100%	100%	131
Risers		6	26-Sep-26	01-Oct-26	25-Feb-26 A	19-Apr-26 A	8,830.52	8,830.52	8,830.52	100%	100%	138
JDH4-02-007	Installation of Irrigation Riser with [Ro	6	26-Sep-26	01-Oct-26	25-Feb-26 A	19-Apr-26 A	8,830.52	8,830.52	8,830.52	100%	100%	138
Potable Network		130	28-Jun-26	06-Oct-26	03-Feb-26 A	27-Jun-26 A	139,057.87	139,057.87	139,057.87	100%	100%	86
Pipe Works		54	28-Jun-26	07-Sep-26	03-Feb-26 A	27-Jun-26 A	84,122.85	84,122.85	84,122.85	100%	100%	62
JDH4-02-007	Excavation and Compaction (FDT) [I	14	28-Jun-26	13-Jul-26	03-Feb-26 A	10-Jun-26 A	8,412.29	8,412.29	8,412.29	100%	100%	28
JDH4-02-007	Sand Bedding [Road 02]	4	14-Jul-26	18-Jul-26	05-Feb-26 A	14-Jun-26 A	4,206.15	4,206.15	4,206.15	100%	100%	29
JDH4-02-007	Installation of HDPE Pipe [Road 02]	10	19-Jul-26	29-Jul-26	09-Feb-26 A	17-Jun-26 A	42,061.41	42,061.41	42,061.41	100%	100%	36
JDH4-02-007	Initial Pressure Test [Road 02]	8	30-Jul-26	08-Aug-26	12-Feb-26 A	20-Jun-26 A	16,824.56	16,824.56	16,824.56	100%	100%	42
JDH4-02-007	Sand Cover & Warning Tape [Road	10	18-Aug-26	29-Aug-26	14-Feb-26 A	21-Jun-26 A	4,206.15	4,206.15	4,206.15	100%	100%	59
JDH4-02-007	Backfilling [Road 02]	8	30-Aug-26	07-Sep-26	15-Feb-26 A	27-Jun-26 A	8,412.29	8,412.29	8,412.29	100%	100%	62
Pipe Encasement		5	08-Sep-26	13-Sep-26	14-Feb-26 A	21-Jun-26 A	6,577.42	6,577.42	6,577.42	100%	100%	72
JDH4-02-007	Encasement for Pipes [Road 02]	5	08-Sep-26	13-Sep-26	14-Feb-26 A	21-Jun-26 A	6,577.42	6,577.42	6,577.42	100%	100%	72
Valves		7	08-Sep-26	15-Sep-26	18-Feb-26 A	25-Mar-26 A	10,512.52	10,512.52	10,512.52	100%	100%	146
JDH4-02-007	Installation of Gate Valves [Road 02]	7	08-Sep-26	15-Sep-26	18-Feb-26 A	25-Mar-26 A	10,512.52	10,512.52	10,512.52	100%	100%	146
Valve Chambers		4	03-Oct-26	06-Oct-26	15-Apr-26 A	02-May-26 A	37,845.08	37,845.08	37,845.08	100%	100%	131
JDH4-02-007	Construction of Air Valve Chambers [	4	03-Oct-26	06-Oct-26	15-Apr-26 A	02-May-26 A	37,845.08	37,845.08	37,845.08	100%	100%	131
Electrical Works		44	07-Oct-26	19-Dec-26	04-Mar-26 A	21-May-26 A	76,122.69	171,249.01	171,249.01	44.45%	100%	177
Telecommunication		44	07-Oct-26	19-Dec-26	04-Mar-26 A	21-May-26 A	76,122.69	171,249.01	171,249.01	44.45%	100%	177
JDH4-02-007	Installation Road Crossing R/F 6 way	21	07-Oct-26	31-Oct-26	13-May-26 A	21-May-26 A	76,122.69	133,214.70	133,214.70	57.14%	100%	135
JDH4-02-007	Installation Road Crossing Un R/F 6	21	01-Nov-26	24-Nov-26	04-Mar-26 A	11-Mar-26 A	0.00	3,973.73	3,973.73	0%	100%	214
JDH4-02-007	Installation of Manholes [Road 02]	21	25-Nov-26	19-Dec-26	25-Mar-26 A	16-May-26 A	0.00	34,060.58	34,060.58	0%	100%	182
Road 10		184	17-May-26	16-Jan-27	05-May-26 A	03-Oct-26 A	608,564.30	908,137.39	908,137.39	67.01%	100%	90
Sewerage Network		41	17-May-26	06-Jul-26	01-Jul-26 A	20-Aug-26 A	419,517.38	419,517.38	419,517.38	100%	100%	-39
Pipe Works		41	17-May-26	06-Jul-26	01-Jul-26 A	11-Aug-26 A	288,229.72	288,229.72	288,229.72	100%	100%	-31
JDH4-02-007	Excavation & Compaction (FDT) [Ro	12	17-May-26	02-Jun-26	01-Jul-26 A	06-Jul-26 A	28,822.98	28,822.98	28,822.98	100%	100%	-29

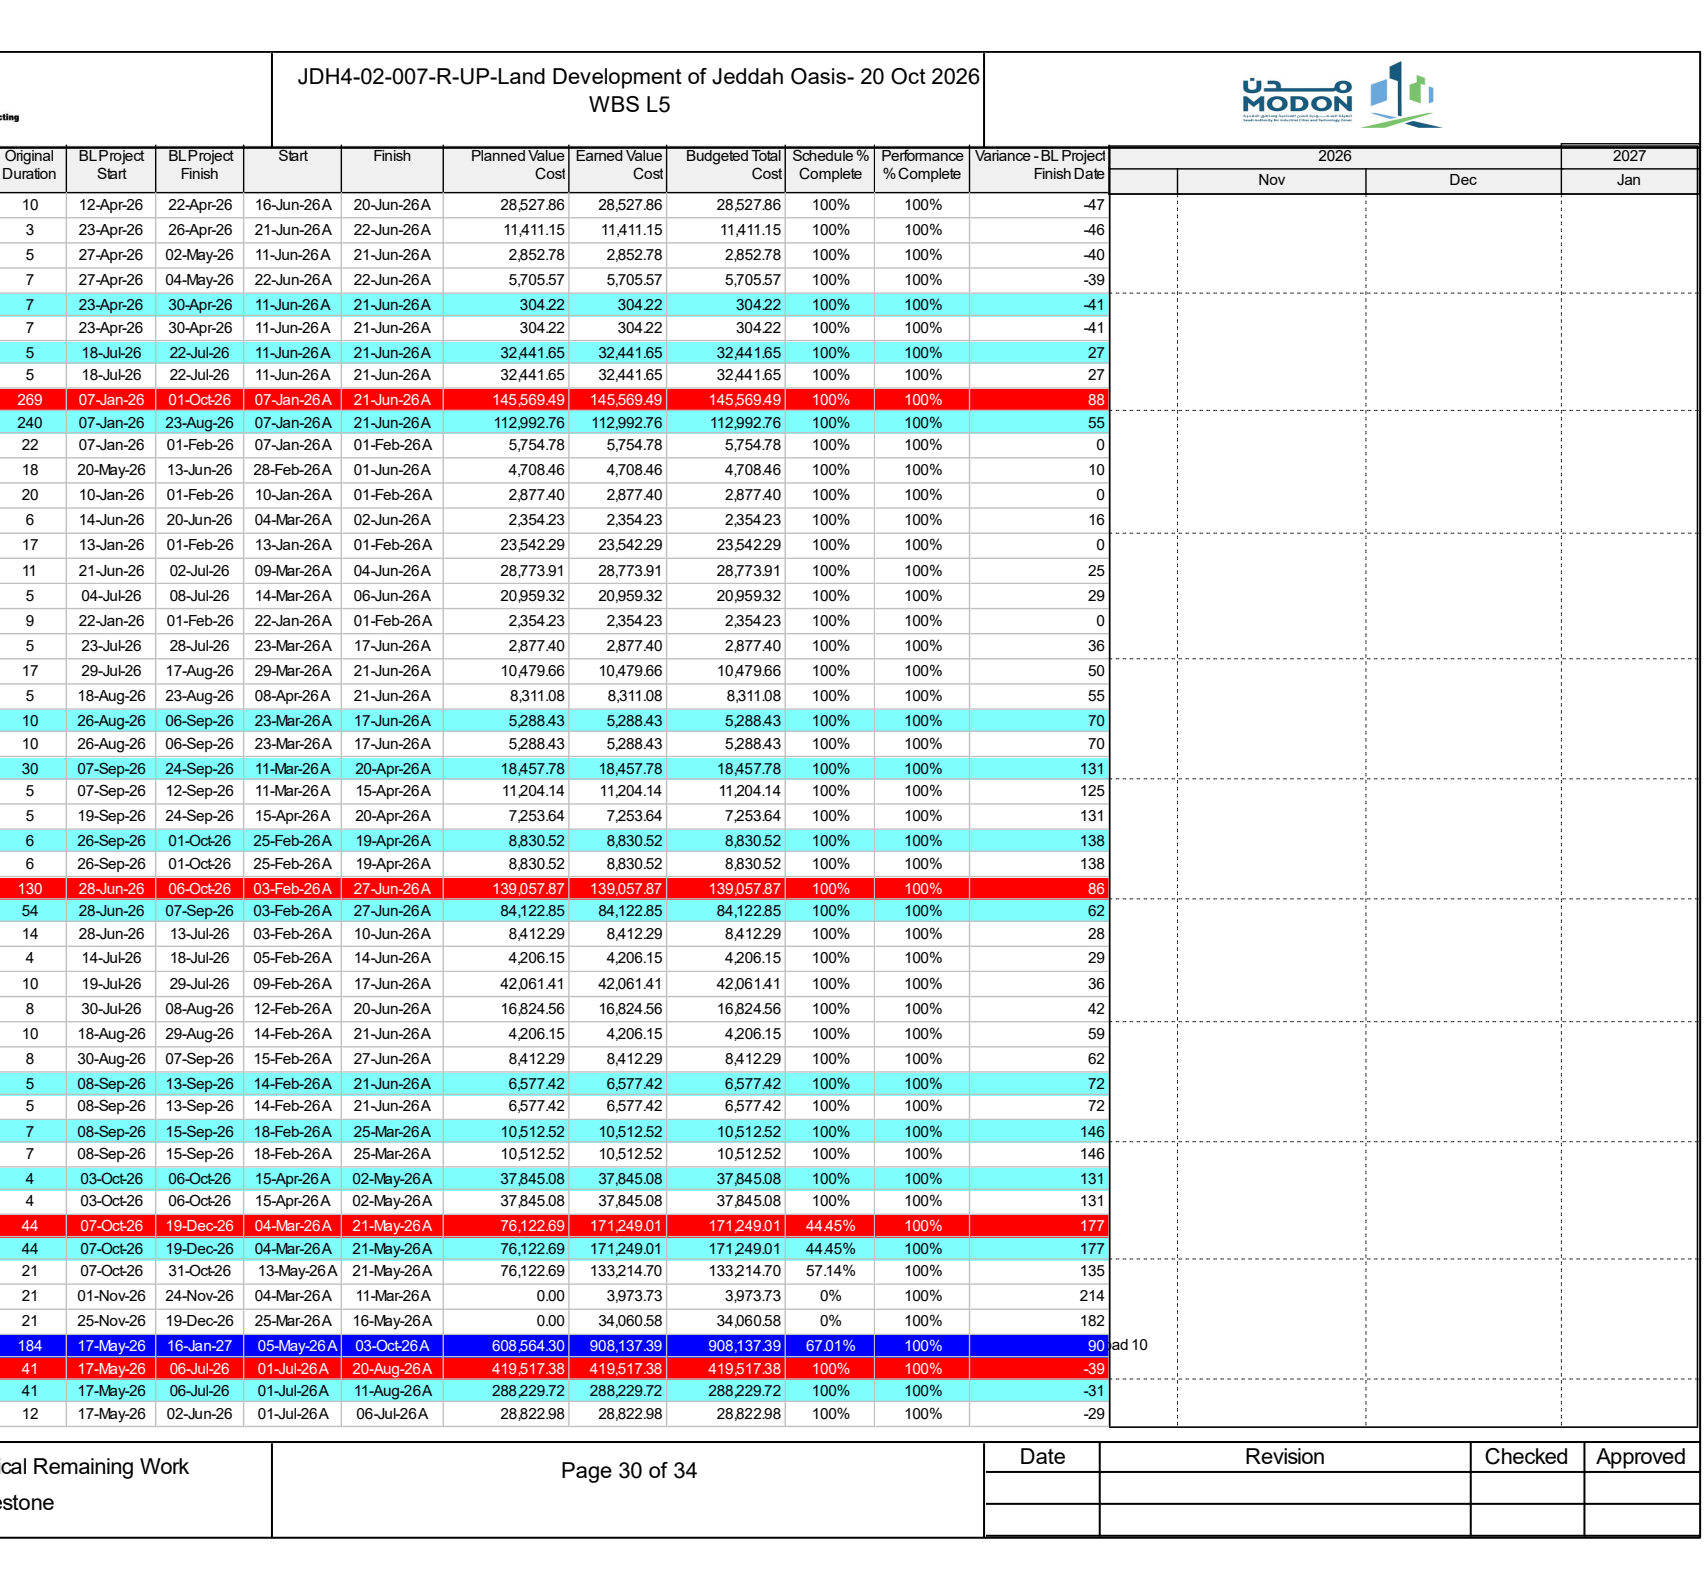

Date	Revision	Checked	Approved


Activity ID	Activity Name	Original Duration	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Schedule % Complete	Performance % Complete	Variance - BL Project Finish Date
JDH4-02-007	Sand Bedding [Road 10]	8	03-Jun-26	11-Jun-26	07-Jul-26 A	15-Jul-26 A	14,411.47	14,411.47	14,411.47	100%	100%	-29
JDH4-02-007	Installation of GRP Pipe [Road 10]	8	13-Jun-26	21-Jun-26	16-Jul-26 A	22-Jul-26 A	144,114.86	144,114.86	144,114.86	100%	100%	-27
JDH4-02-007	Gravity Test [Road 10]	4	22-Jun-26	25-Jun-26	23-Jul-26 A	28-Jul-26 A	57,645.96	57,645.96	57,645.96	100%	100%	-28
JDH4-02-007	Sand Cover & Warning Tape [Road	4	27-Jun-26	30-Jun-26	29-Jul-26 A	05-Aug-26 A	14,411.47	14,411.47	14,411.47	100%	100%	-31
JDH4-02-007	Backfilling & Compaction [Road 10]	5	01-Jul-26	06-Jul-26	06-Aug-26 A	11-Aug-26 A	28,822.98	28,822.98	28,822.98	100%	100%	-31
Pipe Encasement		5	22-Jun-26	27-Jun-26	11-Aug-26 A	18-Aug-26 A	1,521.08	1,521.08	1,521.08	100%	100%	-45
JDH4-02-007	Pipe Encasement Works [Road 10]	5	22-Jun-26	27-Jun-26	11-Aug-26 A	18-Aug-26 A	1,521.08	1,521.08	1,521.08	100%	100%	-45
Manholes		7	28-Jun-26	05-Jul-26	06-Aug-26 A	20-Aug-26 A	129,766.58	129,766.58	129,766.58	100%	100%	-40
JDH4-02-007	Installation of Manholes [Road 10]	7	28-Jun-26	05-Jul-26	06-Aug-26 A	20-Aug-26 A	129,766.58	129,766.58	129,766.58	100%	100%	-40
TSE Network		62	29-Jul-26	07-Nov-26	05-May-26 A	17-Jun-26 A	168,870.75	221,839.87	221,839.87	76.12%	100%	121
Pipe Works		62	29-Jul-26	07-Nov-26	05-May-26 A	04-Jun-26 A	160,529.80	201,483.45	201,483.45	79.67%	100%	132
JDH4-02-007	Excavation and Compaction (FDT) [I	21	29-Jul-26	22-Aug-26	05-May-26 A	10-May-26 A	18,901.67	18,901.67	18,901.67	100%	100%	86
JDH4-02-007	Sand Bedding [Road 10]	21	29-Aug-26	21-Sep-26	11-May-26 A	13-May-26 A	9,450.86	9,450.86	9,450.86	100%	100%	109
JDH4-02-007	Installation of HDPE Pipe [Road 10]	18	22-Sep-26	15-Oct-26	14-May-26 A	17-May-26 A	94,508.42	94,508.42	94,508.42	100%	100%	126
JDH4-02-007	Initial Pressure Test [Road 10]	6	17-Oct-26	22-Oct-26	18-May-26 A	19-May-26 A	25,202.23	37,803.35	37,803.35	66.67%	100%	130
JDH4-02-007	Sand Cover & Warning [Road 10]	8	24-Oct-26	01-Nov-26	21-May-26 A	27-May-26 A	0.00	9,450.86	9,450.86	0%	100%	133
JDH4-02-007	Backfilling & Compaction [Road 10]	11	26-Oct-26	07-Nov-26	30-May-26 A	04-Jun-26 A	0.00	18,901.67	18,901.67	0%	100%	132
JDH4-02-007	Point of Connection [Road 10]	3	17-Oct-26	19-Oct-26	20-May-26 A	20-May-26 A	12,466.62	12,466.62	12,466.62	100%	100%	126
Pipe Encasement		7	17-Oct-26	24-Oct-26	02-Jun-26 A	17-Jun-26 A	5,353.18	9,368.07	9,368.07	57.14%	100%	109
JDH4-02-007	Encasement for Pipes [Road 10]	7	17-Oct-26	24-Oct-26	02-Jun-26 A	17-Jun-26 A	5,353.18	9,368.07	9,368.07	57.14%	100%	109
Valves		11	17-Oct-26	28-Oct-26	20-May-26 A	04-Jun-26 A	2,987.77	10,988.35	10,988.35	27.19%	100%	124
JDH4-02-007	Installation of Gate Valves [Road 10]	5	17-Oct-26	21-Oct-26	20-May-26 A	04-Jun-26 A	2,987.77	3,734.71	3,734.71	80%	100%	118
JDH4-02-007	Installation of Air Valves [Road 10]	6	22-Oct-26	28-Oct-26	21-May-26 A	04-Jun-26 A	0.00	7,253.64	7,253.64	0%	100%	124
Potable Network		61	23-Aug-26	08-Nov-26	10-Jun-26 A	02-Jul-26 A	16,598.08	62,644.01	62,644.01	26.5%	100%	109
Pipe Works		61	23-Aug-26	08-Nov-26	10-Jun-26 A	26-Jun-26 A	16,598.08	20,491.46	20,491.46	81%	100%	115
JDH4-02-007	Excavation and Compaction (FDT) [I	17	23-Aug-26	10-Sep-26	10-Jun-26 A	13-Jun-26 A	2,049.15	2,049.15	2,049.15	100%	100%	77
JDH4-02-007	Sand Bedding [Road 10]	15	12-Sep-26	29-Sep-26	14-Jun-26 A	15-Jun-26 A	1,024.57	1,024.57	1,024.57	100%	100%	90
JDH4-02-007	Installation of HDPE Pipe [Road 10]	14	30-Sep-26	15-Oct-26	17-Jun-26 A	19-Jun-26 A	10,245.73	10,245.73	10,245.73	100%	100%	101
JDH4-02-007	Initial Pressure Test [Road 10]	5	17-Oct-26	21-Oct-26	19-Jun-26 A	21-Jun-26 A	3,278.63	4,098.29	4,098.29	80%	100%	104
JDH4-02-007	Sand Cover & Warning Tape [Road	9	29-Oct-26	08-Nov-26	21-Jun-26 A	24-Jun-26 A	0.00	1,024.57	1,024.57	0%	100%	116
JDH4-02-007	Backfilling [Road 10]	9	29-Oct-26	08-Nov-26	22-Jun-26 A	26-Jun-26 A	0.00	2,049.15	2,049.15	0%	100%	115
Pipe Encasement		5	25-Oct-26	29-Oct-26	21-Jun-26 A	24-Jun-26 A	0.00	1,679.34	1,679.34	0%	100%	108
JDH4-02-007	Encasement for Pipes [Road 10]	5	25-Oct-26	29-Oct-26	21-Jun-26 A	24-Jun-26 A	0.00	1,679.34	1,679.34	0%	100%	108
Valves		6	29-Oct-26	04-Nov-26	27-Jun-26 A	30-Jun-26 A	0.00	2,628.13	2,628.13	0%	100%	108
JDH4-02-007	Installation of Gate Valves [Road 10]	6	29-Oct-26	04-Nov-26	27-Jun-26 A	30-Jun-26 A	0.00	2,628.13	2,628.13	0%	100%	108
Valve Chambers		8	31-Oct-26	08-Nov-26	24-Jun-26 A	02-Jul-26 A	0.00	37,845.08	37,845.08	0%	100%	109
JDH4-02-007	Construction of Air Valve Chambers [	8	31-Oct-26	08-Nov-26	24-Jun-26 A	02-Jul-26 A	0.00	37,845.08	37,845.08	0%	100%	109
Electrical Works		155	17-Oct-26	16-Jan-27	04-Jul-26 A	03-Oct-26 A	3,578.08	204,136.13	204,136.13	1.75%	100%	90
MV & LV Cables		22	17-Oct-26	22-Nov-26	16-Sep-26 A	03-Oct-26 A	3,578.08	36,633.78	36,633.78	9.77%	100%	43
Low Voltage Cable		22	17-Oct-26	22-Nov-26	16-Sep-26 A	03-Oct-26 A	3,578.08	36,633.78	36,633.78	9.77%	100%	43
JDH4-02-00	Excavation for Low Voltage Cable [R	11	17-Oct-26	28-Oct-26	16-Sep-26 A	24-Sep-26 A	3,578.08	9,839.72	9,839.72	36.36%	100%	29
JDH4-02-00	Installation of Low Voltage Cables [R	11	10-Nov-26	22-Nov-26	23-Sep-26 A	03-Oct-26 A	0.00	26,794.06	26,794.06	0%	100%	43
Telecommunication		84	29-Oct-26	16-Jan-27	04-Jul-26 A	21-Aug-26 A	0.00	167,502.35	167,502.35	0%	100%	126
JDH4-02-007	Installation Road Crossing R/F 6 way	19	29-Oct-26	19-Nov-26	04-Jul-26 A	03-Aug-26 A	0.00	76,068.62	76,068.62	0%	100%	92
JDH4-02-007	Installation Road Crossing Un R/F 6	16	24-Nov-26	12-Dec-26	12-Jul-26 A	04-Aug-26 A	0.00	3,406.06	3,406.06	0%	100%	110
JDH4-02-007	Installation of 2 x 32 mm diameter HI	17	16-Dec-26	04-Jan-27	25-Jul-26 A	21-Aug-26 A	0.00	70,997.38	70,997.38	0%	100%	116
JDH4-02-007	Installation of Manholes [Road 10]	10	05-Jan-27	16-Jan-27	25-Jul-26 A	11-Aug-26 A	0.00	17,030.29	17,030.29	0%	100%	134
Out of Zone		42	17-Oct-26	03-Dec-26	18-Jul-26 A	03-Oct-26 A	2,523.01	49,496.57	49,496.57	5.1%	100%	53
Electrical Works		42	17-Oct-26	03-Dec-26	18-Jul-26 A	03-Oct-26 A	2,523.01	49,496.57	49,496.57	5.1%	100%	53
LV Cables		42	17-Oct-26	03-Dec-26	18-Jul-26 A	03-Oct-26 A	2,523.01	49,496.57	49,496.57	5.1%	100%	53
Low Voltage Cable		42	17-Oct-26	03-Dec-26	18-Jul-26 A	03-Oct-26 A	2,523.01	49,496.57	49,496.57	5.1%	100%	53

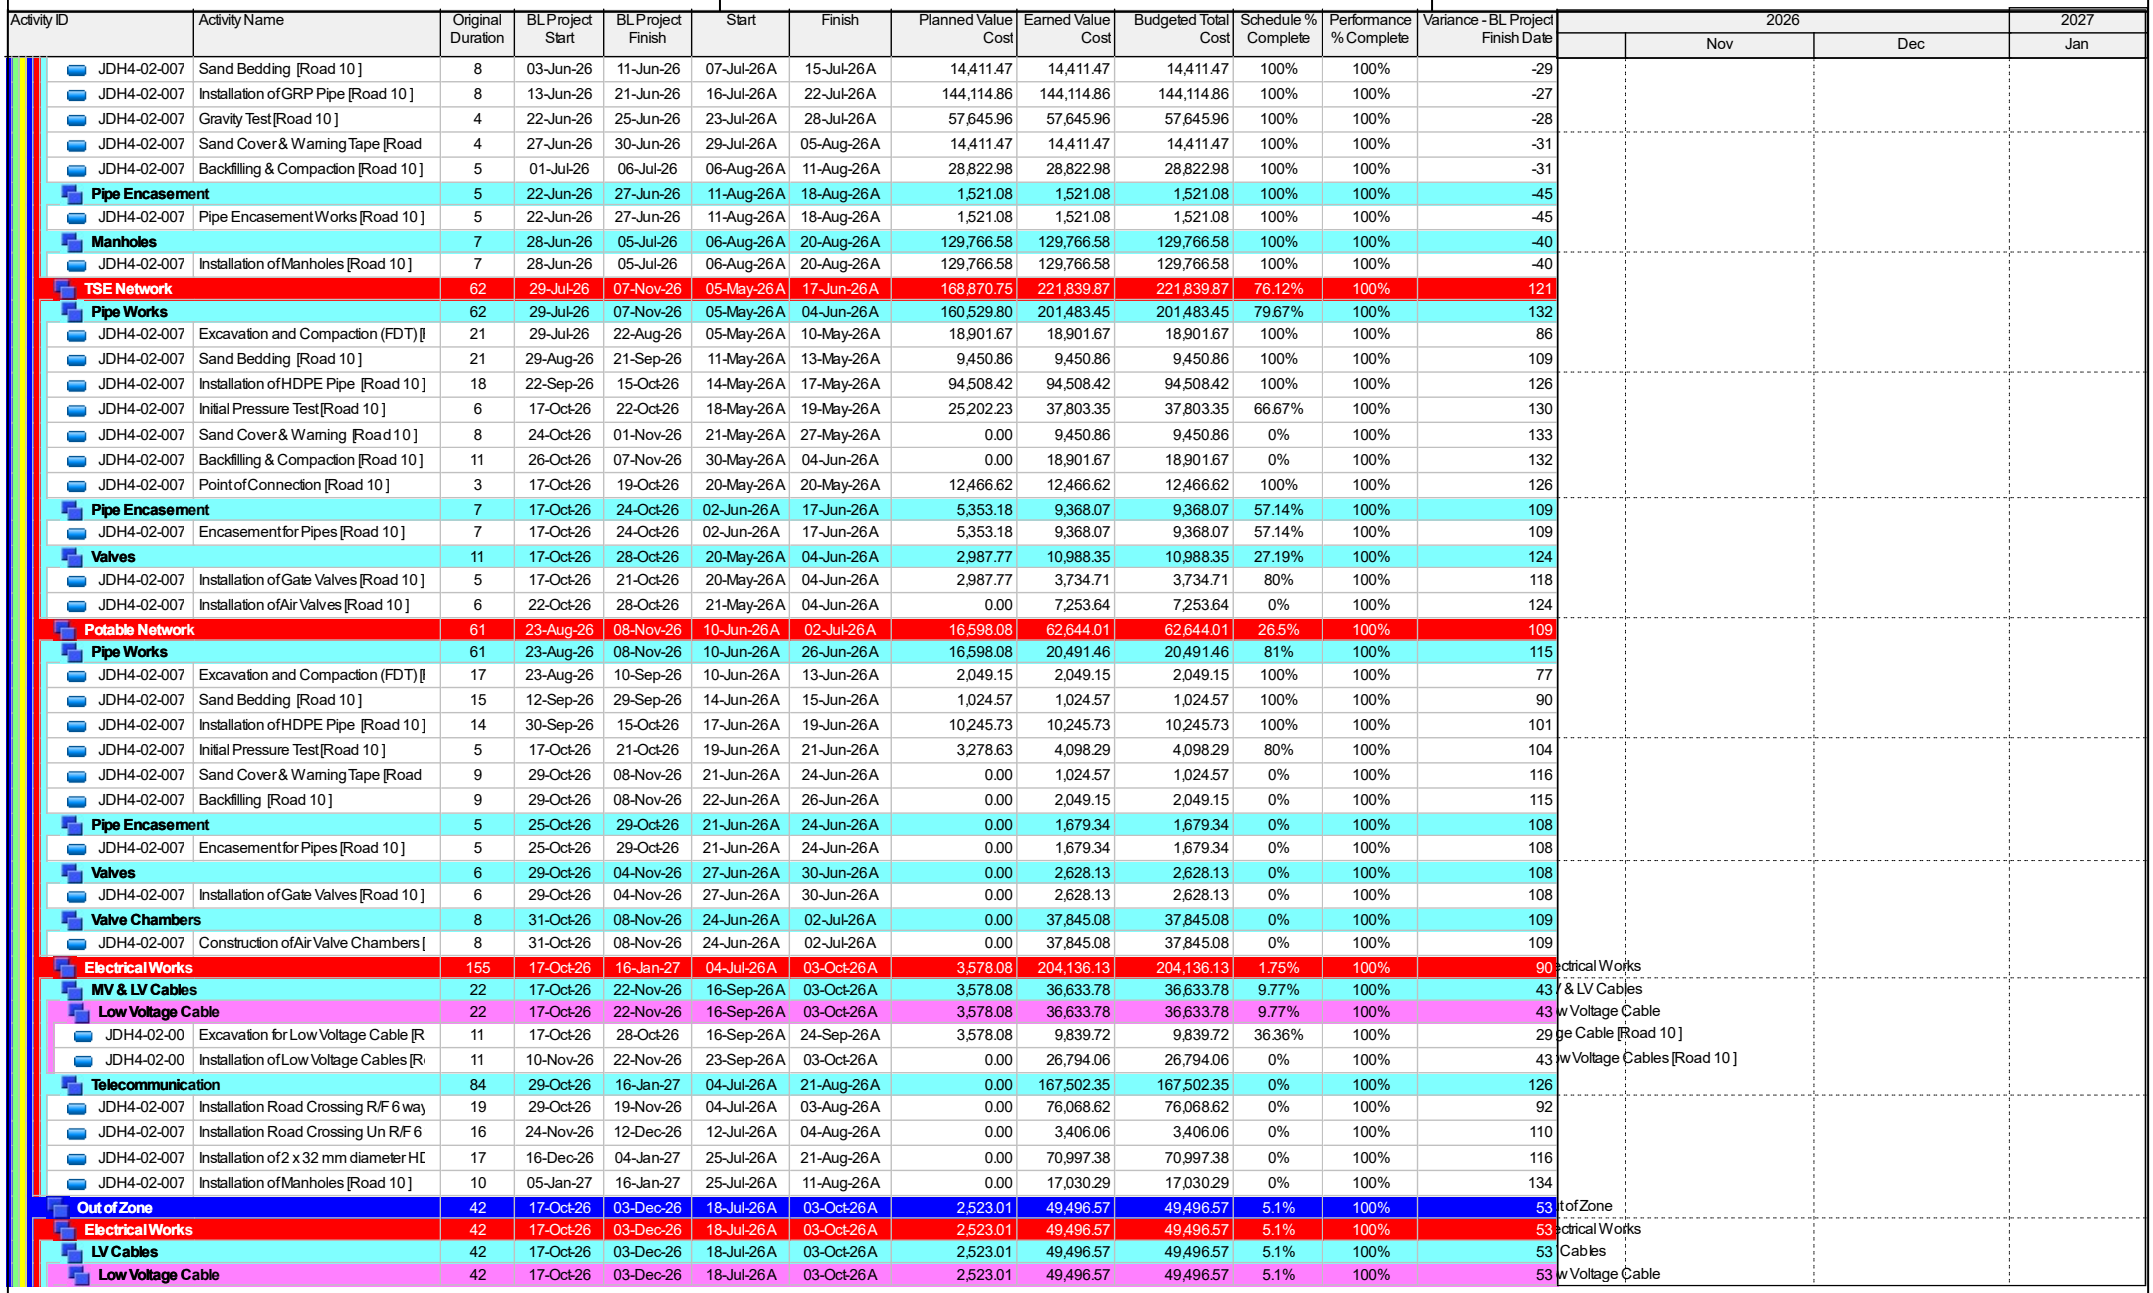

Actual Work
Remaining Work
Critical Remaining Work
Milestone

Date	Revision	Checked	Approved


Activity ID	Activity Name	Original Duration	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Schedule % Complete	Performance % Complete	Variance - BL Project Finish Date
JDH4-02-00	Excavation for Low Voltage Cable [O	21	17-Oct-26	09-Nov-26	18-Jul-26 A	30-Sep-26 A	2,523.01	13,245.78	13,245.78	19.05%	100%	35
JDH4-02-00	Installation of Low Voltage Cables [O	21	10-Nov-26	03-Dec-26	26-Jul-26 A	03-Oct-26 A	0.00	36,250.79	36,250.79	0%	100%	53
Sewage Lift Station		147	06-Sep-26	02-May-27	22-Apr-26 A	29-Dec-26	8,830.53	2,215,510.09	3,049,343.44	0.29%	72.66%	102
Site Works		25	06-Sep-26	24-Oct-26	14-May-26 A	30-Jul-26 A	8,830.53	10,249.72	10,249.72	86.15%	100%	72
JDH4-02-007-C	Excavation [Sewage Lift Station]	20	06-Sep-26	29-Sep-26	14-May-26 A	16-May-26 A	3,942.20	3,942.20	3,942.20	100%	100%	114
JDH4-02-007-C	Backfilling [Sewage Lift Station]	11	30-Sep-26	12-Oct-26	08-Jun-26 A	30-Jul-26 A	1,576.88	1,576.88	1,576.88	100%	100%	62
JDH4-02-007-C	Install gravel beddings [Sewage Lift S	10	13-Oct-26	24-Oct-26	06-Jun-26 A	08-Jun-26 A	3,311.45	4,730.64	4,730.64	70%	100%	118
Concrete Works		27	25-Oct-26	24-Nov-26	07-May-26 A	24-May-26 A	0.00	67,679.63	67,679.63	0%	100%	155
JDH4-02-007-C	Lean concrete under the foundations	8	25-Oct-26	02-Nov-26	07-May-26 A	07-May-26 A	0.00	2,081.48	2,081.48	0%	100%	150
JDH4-02-007-C	Footings For Sewage Lift Station [Se	8	03-Nov-26	11-Nov-26	09-May-26 A	09-May-26 A	0.00	25,230.06	25,230.06	0%	100%	157
JDH4-02-007-C	Cast concrete for trench Including Ma	11	12-Nov-26	24-Nov-26	10-May-26 A	24-May-26 A	0.00	40,368.09	40,368.09	0%	100%	155
Thermal & Moisture Protection		10	25-Nov-26	06-Dec-26	31-May-26 A	07-Jun-26 A	0.00	7,001.35	7,001.35	0%	100%	156
JDH4-02-007-C	Install 250 micron polyethylene shee	5	25-Nov-26	30-Nov-26	31-May-26 A	01-Jun-26 A	0.00	2,270.71	2,270.71	0%	100%	156
JDH4-02-007-C	Applying 2 Coats of Bituminous Pain	5	01-Dec-26	06-Dec-26	01-Jun-26 A	07-Jun-26 A	0.00	4,730.64	4,730.64	0%	100%	156
Metals		6	12-Nov-26	18-Nov-26	26-Sep-26 A	01-Oct-26 A	0.00	10,092.02	10,092.02	0%	100%	41
JDH4-02-007-C	Install Stainless steel [Sewage Lift St	6	12-Nov-26	18-Nov-26	26-Sep-26 A	01-Oct-26 A	0.00	10,092.02	10,092.02	0%	100%	41
Mechanical Works		109	12-Nov-26	21-Jan-27	22-Apr-26 A	01-Nov-26	0.00	1,354,219.78	1,705,863.69	0%	79.39%	70
Pipes & Fittings		76	12-Nov-26	21-Jan-27	23-Apr-26 A	30-Sep-26 A	0.00	256,712.33	256,712.33	0%	100%	97
JDH4-02-007-	Installation of Pipes & Fittings [Sewag	14	12-Nov-26	28-Nov-26	23-Apr-26 A	10-Aug-26 A	0.00	30,587.94	30,587.94	0%	100%	93
JDH4-02-007-	Installation of Gate Valves [Sewage L	9	29-Nov-26	08-Dec-26	23-Apr-26 A	18-Aug-26 A	0.00	29,014.56	29,014.56	0%	100%	95
JDH4-02-007-	Installation of Dismantling Joints [Sev	8	09-Dec-26	17-Dec-26	25-Apr-26 A	24-Sep-26 A	0.00	13,876.54	13,876.54	0%	100%	72
JDH4-02-007-	Installation of Non Return Valve DN2	9	19-Dec-26	28-Dec-26	25-Apr-26 A	26-Apr-26 A	0.00	9,461.27	9,461.27	0%	100%	208
JDH4-02-007-	Installation of Air Valve DN60 [Sewag	8	29-Dec-26	06-Jan-27	25-Apr-26 A	26-Apr-26 A	0.00	11,353.53	11,353.53	0%	100%	216
JDH4-02-007-	Installation of Bauer Coupling DN15(	6	07-Jan-27	13-Jan-27	15-Sep-26 A	30-Sep-26 A	0.00	4,730.64	4,730.64	0%	100%	90
JDH4-02-007-	Installation of Odors scrubbing syster	7	14-Jan-27	21-Jan-27	05-Jul-26 A	23-Aug-26 A	0.00	157,687.85	157,687.85	0%	100%	129
Control Equipment		97	29-Nov-26	11-Jan-27	22-Apr-26 A	30-Sep-26 A	0.00	118,265.89	118,265.89	0%	100%	88
JDH4-02-007-	Installation of Manually operated dav	8	29-Nov-26	07-Dec-26	03-Sep-26 A	07-Sep-26 A	0.00	94,612.71	94,612.71	0%	100%	77
JDH4-02-007-	Installation of Air Vents [Sewage Lift S	7	17-Dec-26	24-Dec-26	02-Sep-26 A	07-Sep-26 A	0.00	4,730.64	4,730.64	0%	100%	92
JDH4-02-007-	Installation of Screening Container [S	8	26-Dec-26	03-Jan-27	22-Apr-26 A	25-Apr-26 A	0.00	9,461.27	9,461.27	0%	100%	214
JDH4-02-007-	Installation of Baffle Plates [Sewage L	7	04-Jan-27	11-Jan-27	23-Sep-26 A	30-Sep-26 A	0.00	9,461.27	9,461.27	0%	100%	88
Interface Works		3	08-Dec-26	10-Dec-26	02-Sep-26 A	23-Sep-26 A	0.00	63,075.14	63,075.14	0%	100%	67
JDH4-02-007-	Interfacing Works [Sewage Lift Statio	3	08-Dec-26	10-Dec-26	02-Sep-26 A	23-Sep-26 A	0.00	63,075.14	63,075.14	0%	100%	67
Anti Water Hammer Equipment		4	12-Dec-26	15-Dec-26	01-Oct-26 A	25-Oct-26	0.00	706,441.58	883,051.97	0%	80%	44
JDH4-02-007-	Installation of Anti-Water Hammer Ec	4	12-Dec-26	15-Dec-26	01-Oct-26 A	25-Oct-26	0.00	706,441.58	883,051.97	0%	80%	44
Air Conditioning & Ventilation		6	12-Jan-27	18-Jan-27	28-Sep-26 A	01-Oct-26 A	0.00	18,922.54	18,922.54	0%	100%	93
JDH4-02-007-	Installation of Air Conditioning [Sewag	6	12-Jan-27	18-Jan-27	28-Sep-26 A	01-Oct-26 A	0.00	18,922.54	18,922.54	0%	100%	93
Fuel System		17	16-Dec-26	04-Jan-27	15-Aug-26 A	25-Aug-26 A	0.00	75,690.17	75,690.17	0%	100%	112
JDH4-02-007-	Installation of Bulk Fuel storage tank,	5	16-Dec-26	21-Dec-26	15-Aug-26 A	25-Aug-26 A	0.00	18,922.54	18,922.54	0%	100%	100
JDH4-02-007-	Installation of Fuel pump set , 1 duty a	6	22-Dec-26	28-Dec-26	15-Aug-26 A	25-Aug-26 A	0.00	47,306.36	47,306.36	0%	100%	106
JDH4-02-007-	Pipes and Fitting Works [Sewage Lift	6	29-Dec-26	04-Jan-27	15-Aug-26 A	25-Aug-26 A	0.00	9,461.27	9,461.27	0%	100%	112
Fire Fighting		9	29-Dec-26	21-Jan-27	23-Sep-26 A	26-Sep-26 A	0.00	56,767.63	56,767.63	0%	100%	101
JDH4-02-007-	Installation of Fire fighting for electrica	5	29-Dec-26	03-Jan-27	23-Sep-26 A	26-Sep-26 A	0.00	47,306.36	47,306.36	0%	100%	85
JDH4-02-007-	Installation of Foam type - wheeled ty	3	19-Jan-27	21-Jan-27	24-Sep-26 A	26-Sep-26 A	0.00	9,461.27	9,461.27	0%	100%	101
Pumps		6	04-Jan-27	10-Jan-27	23-Sep-26 A	01-Nov-26	0.00	58,344.51	233,378.02	0%	25%	60
JDH4-02-007-	Installation of Submersible pump [Se	6	04-Jan-27	10-Jan-27	23-Sep-26 A	01-Nov-26	0.00	58,344.51	233,378.02	0%	25%	60
Electrical Works		141	12-Dec-26	02-May-27	01-Sep-26 A	29-Dec-26	0.00	748,024.48	1,230,213.92	0%	60.8%	102
Main Distribution Board		14	12-Dec-26	27-Dec-26	03-Oct-26 A	05-Nov-26	0.00	52,036.99	104,073.98	0%	50%	44
JDH4-02-007-	Installation of Main Distribution Board	7	12-Dec-26	19-Dec-26	03-Oct-26 A	28-Oct-26	0.00	37,845.09	75,690.17	0%	50%	44
JDH4-02-007-	Installation of Panel Board [Sewage I	7	20-Dec-26	27-Dec-26	03-Oct-26 A	05-Nov-26	0.00	14,191.91	28,383.81	0%	50%	44
Local Control Panel		25	20-Dec-26	27-Jan-27	04-Oct-26 A	21-Nov-26	0.00	53,613.87	107,227.74	0%	50%	58
JDH4-02-007-	Installation of MCP-LP-01 [Sewage L	10	20-Dec-26	30-Dec-26	04-Oct-26 A	09-Nov-26	0.00	12,615.03	25,230.06	0%	50%	44

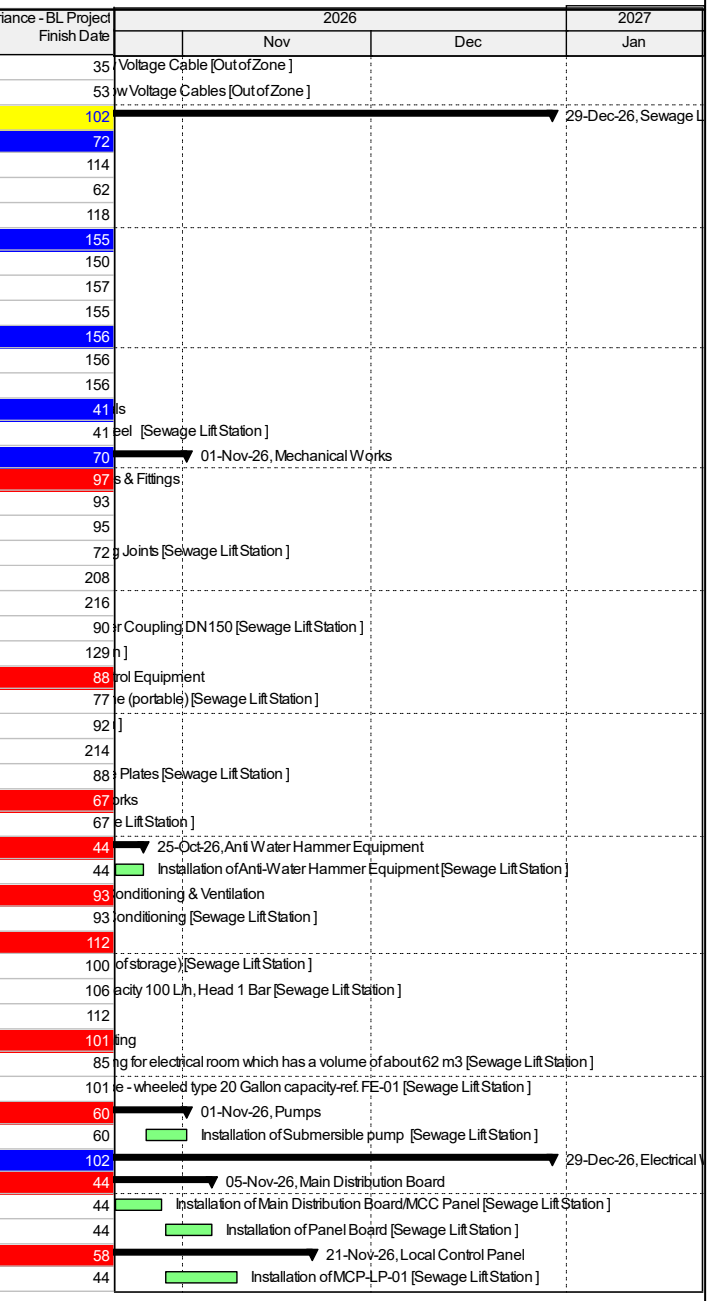

Actual Work | Critical Remaining Work | Remaining Work | Milestone

Date	Revision	Checked	Approved


Activity ID	Activity Name	Original Duration	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Schedule % Complete	Performance % Complete	Variance - BL Project Finish Date
JDH4-02-007-	Installation of MCP-LP-02 [Sewage L	5	31-Dec-26	05-Jan-27	04-Oct-26 A	15-Nov-26	0.00	12,615.03	25,230.06	0%	50%	44
JDH4-02-007-	Installation of OD-CP [Sewage Lift St	5	06-Jan-27	11-Jan-27	04-Oct-26 A	16-Nov-26	0.00	14,191.91	28,383.81	0%	50%	49
JDH4-02-007-	Installation of FP-CP [Sewage Lift Sta	5	23-Jan-27	27-Jan-27	04-Oct-26 A	21-Nov-26	0.00	14,191.91	28,383.81	0%	50%	58
Diesel Generator		10	31-Dec-26	11-Jan-27	15-Sep-26 A	17-Sep-26 A	0.00	75,690.17	75,690.17	0%	100%	98
JDH4-02-007-	Installation of Standby Diesel Genera	10	31-Dec-26	11-Jan-27	15-Sep-26 A	17-Sep-26 A	0.00	75,690.17	75,690.17	0%	100%	98
Power Factor Correction Capacitor Bank		7	12-Jan-27	19-Jan-27	05-Oct-26 A	17-Nov-26	0.00	11,038.15	22,076.30	0%	50%	54
JDH4-02-007-	Installation of Power Factor Correctio	7	12-Jan-27	19-Jan-27	05-Oct-26 A	17-Nov-26	0.00	11,038.15	22,076.30	0%	50%	54
Low-Voltage Electrical Power Conductors and Cable		9	20-Jan-27	30-Jan-27	29-Sep-26 A	28-Nov-26	0.00	8,767.60	17,535.20	0%	50%	54
JDH4-02-007-	Installation of Low Voltage Cables [Se	9	20-Jan-27	30-Jan-27	29-Sep-26 A	28-Nov-26	0.00	8,767.60	17,535.20	0%	50%	54
Wiring Devices		5	31-Jan-27	04-Feb-27	02-Sep-26 A	07-Sep-26 A	0.00	5,044.14	5,044.14	0%	100%	128
JDH4-02-007-	Installation of Wiring Devices [Sewag	5	31-Jan-27	04-Feb-27	02-Sep-26 A	07-Sep-26 A	0.00	5,044.14	5,044.14	0%	100%	128
Enclosed Switches and Circuit Breakers		5	12-Jan-27	17-Jan-27	14-Oct-26 A	15-Nov-26	0.00	5,033.40	8,830.52	0%	57%	54
JDH4-02-007-	Installation of Enclosed Switches and	5	12-Jan-27	17-Jan-27	14-Oct-26 A	15-Nov-26	0.00	5,033.40	8,830.52	0%	57%	54
Lighting		6	18-Jan-27	24-Jan-27	08-Sep-26 A	29-Sep-26 A	0.00	16,399.53	16,399.53	0%	100%	100
JDH4-02-007-	Installation of Lightings [Sewage Lift S	6	18-Jan-27	24-Jan-27	08-Sep-26 A	29-Sep-26 A	0.00	16,399.53	16,399.53	0%	100%	100
Grounding and Bonding for Electrical Systems		6	25-Jan-27	31-Jan-27	16-Nov-26	22-Nov-26	0.00	0.00	18,607.15	0%	0%	60
JDH4-02-007-	Installation of Grounding Links [Sewa	6	25-Jan-27	31-Jan-27	16-Nov-26	22-Nov-26	0.00	0.00	18,607.15	0%	0%	60
Electrical Manholes		6	01-Feb-27	07-Feb-27	02-Sep-26 A	08-Sep-26 A	0.00	10,723.17	10,723.17	0%	100%	129
JDH4-02-007-	Installation of Electrical Manholes [Se	6	01-Feb-27	07-Feb-27	02-Sep-26 A	08-Sep-26 A	0.00	10,723.17	10,723.17	0%	100%	129
ICT (Data& telephone System)		19	08-Feb-27	14-Mar-27	05-Oct-26 A	16-Dec-26	0.00	22,076.30	44,152.59	0%	50%	71
JDH4-02-007-	Installation of IDF Cabinet 9U (for dat	10	08-Feb-27	18-Feb-27	05-Oct-26 A	18-Oct-26 A	0.00	22,076.30	22,076.30	0%	100%	106
JDH4-02-007-	Installationof Single data/Telephone	5	20-Feb-27	25-Feb-27	29-Nov-26	03-Dec-26	0.00	0.00	1,261.50	0%	0%	71
JDH4-02-007-	Installation of Data Switch (24 Port) [S	5	27-Feb-27	03-Mar-27	05-Dec-26	09-Dec-26	0.00	0.00	18,922.54	0%	0%	71
JDH4-02-007-	Installation of Fiber optic cable (12 Co	6	04-Mar-27	14-Mar-27	10-Dec-26	16-Dec-26	0.00	0.00	1,892.25	0%	0%	71
Security System (CCTV System)		13	27-Feb-27	16-Mar-27	20-Sep-26 A	27-Sep-26 A	0.00	198,686.69	198,686.69	0%	100%	142
JDH4-02-007-	Installation of 5.0 Megapixel, Fixed bu	13	27-Feb-27	16-Mar-27	20-Sep-26 A	27-Sep-26 A	0.00	198,686.69	198,686.69	0%	100%	142
Duct Bank and Handhole For Telecom Network		17	17-Mar-27	05-Apr-27	01-Sep-26 A	03-Oct-26 A	0.00	8,199.77	8,199.77	0%	100%	154
JDH4-02-007-	Installation of 2 x 50mm HDPE ducts	12	17-Mar-27	30-Mar-27	01-Sep-26 A	03-Oct-26 A	0.00	5,046.01	5,046.01	0%	100%	149
JDH4-02-007-	Installation of Handholes (800x800x	5	31-Mar-27	05-Apr-27	01-Sep-26 A	03-Oct-26 A	0.00	3,153.76	3,153.76	0%	100%	154
Programmable Logic Controllers		14	31-Mar-27	15-Apr-27	04-Oct-26 A	20-Dec-26	0.00	126,150.28	252,300.56	0%	50%	96
JDH4-02-007-	Installation of Programmable Logic C	14	31-Mar-27	15-Apr-27	04-Oct-26 A	20-Dec-26	0.00	126,150.28	252,300.56	0%	50%	96
Process Control Wiring		4	17-Apr-27	20-Apr-27	18-Oct-26 A	24-Dec-26	0.00	63,075.14	157,687.85	0%	40%	96
JDH4-02-007-	Installation of Process Control Wiring	4	17-Apr-27	20-Apr-27	18-Oct-26 A	24-Dec-26	0.00	63,075.14	157,687.85	0%	40%	96
Instrumentation for Process Systems		8	21-Apr-27	02-May-27	17-Sep-26 A	29-Dec-26	0.00	91,489.28	182,978.56	0%	50%	102
JDH4-02-007-	Installation of Process System [Sewa	8	21-Apr-27	02-May-27	17-Sep-26 A	29-Dec-26	0.00	91,489.28	182,978.56	0%	50%	102
Fence Work		20	27-Feb-27	12-Apr-27	23-Sep-26 A	27-Sep-26 A	0.00	18,243.11	18,243.11	0%	100%	165
JDH4-02-007-C	Installation of Chain Link Fence [Sew	20	27-Feb-27	24-Mar-27	23-Sep-26 A	26-Sep-26 A	0.00	11,984.28	11,984.28	0%	100%	150
JDH4-02-007-C	Installation of Pedestrian Gate [Sewa	16	25-Mar-27	12-Apr-27	26-Sep-26 A	27-Sep-26 A	0.00	6,258.83	6,258.83	0%	100%	165
MV Cable Works		192	02-Jan-27	06-May-27	13-May-26 A	13-Oct-26 A	0.00	888,341.63	888,341.63	0%	100%	172
Medium Voltage Cable Road 8		68	02-Jan-27	06-Mar-27	13-May-26 A	09-Aug-26 A	0.00	165,937.27	165,937.27	0%	100%	177
JDH4-02-007-C	Excavation for Trench [Road 08]	13	02-Jan-27	16-Jan-27	06-Jun-26 A	30-Jun-26 A	0.00	7,545.00	7,545.00	0%	100%	170
JDH4-02-007-C	Installation of Duct banks [Road 08]	21	17-Jan-27	09-Feb-27	13-May-26 A	21-Jun-26 A	0.00	31,916.02	31,916.02	0%	100%	199
JDH4-02-007-C	Installation of Medium Voltage Cable	20	10-Feb-27	06-Mar-27	05-Jul-26 A	09-Aug-26 A	0.00	126,476.25	126,476.25	0%	100%	177
Medium Voltage Cable Road 7		43	07-Jan-27	29-Mar-27	13-May-26 A	02-Aug-26 A	0.00	130,128.34	130,128.34	0%	100%	200
JDH4-02-007-C	Excavation for Trench [Road 07-N]	11	07-Jan-27	19-Jan-27	18-Jun-26 A	27-Jul-26 A	0.00	6,530.33	6,530.33	0%	100%	151
JDH4-02-007-C	Installation of Duct banks [Road 07-N	21	20-Jan-27	13-Feb-27	13-May-26 A	26-May-26 A	0.00	13,876.53	13,876.53	0%	100%	222
JDH4-02-007-C	Installation of Medium Voltage Cable	17	07-Mar-27	29-Mar-27	28-Jul-26 A	02-Aug-26 A	0.00	109,721.48	109,721.48	0%	100%	200
Medium Voltage Cable Road 1		56	20-Jan-27	30-Mar-27	25-Jul-26 A	18-Aug-26 A	0.00	264,999.32	264,999.32	0%	100%	187
JDH4-02-007-C	Excavation for Trench [Road 01]	21	20-Jan-27	13-Feb-27	25-Jul-26 A	18-Aug-26 A	0.00	13,372.86	13,372.86	0%	100%	152
JDH4-02-007-C	Installation of Duct banks [Road 01]	21	14-Feb-27	14-Mar-27	25-Jul-26 A	18-Aug-26 A	0.00	27,290.51	27,290.51	0%	100%	173
JDH4-02-007-C	Installation of Medium Voltage Cable	14	15-Mar-27	30-Mar-27	28-Jul-26 A	18-Aug-26 A	0.00	224,335.95	224,335.95	0%	100%	187

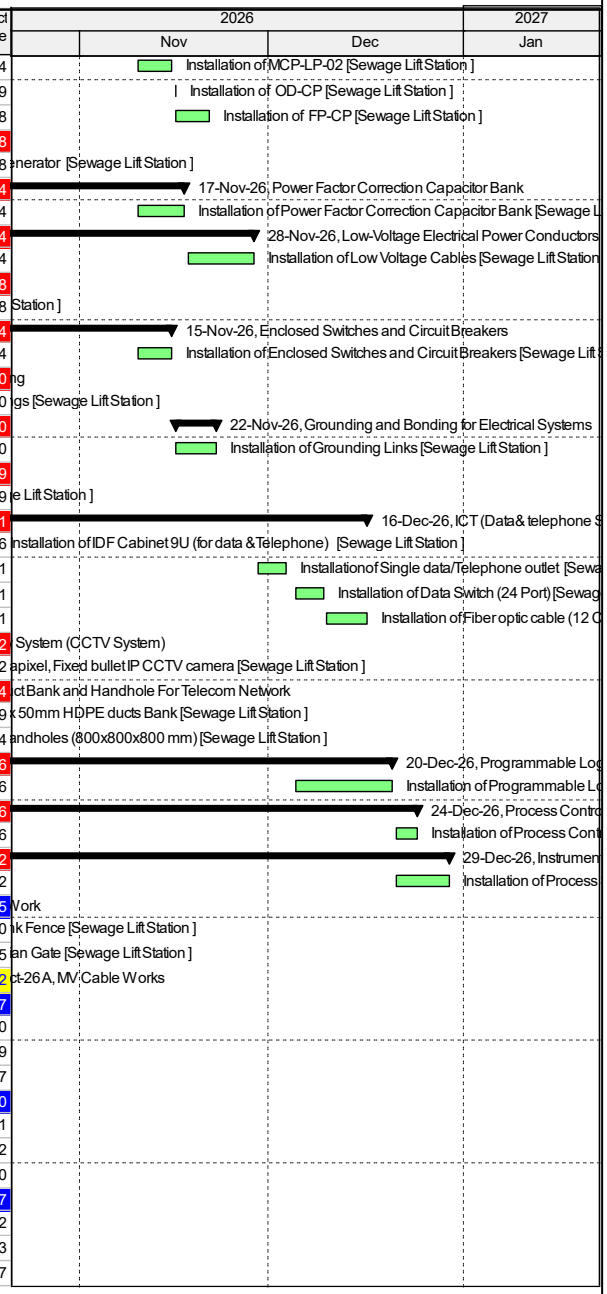

Actual Work
Remaining Work
Critical Remaining Work
Milestone

Date	Revision	Checked	Approved

Activity ID	Activity Name	Original Duration	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Schedule % Complete	Performance % Complete	Variance - BL Project Finish Date
Medium Voltage Cable Road 10		54	26-Jan-27	25-Apr-27	10-Aug-26 A	23-Aug-26 A	0.00	130,978.55	130,978.55	0%	100%	206
JDH4-02-007-C	Excavation for Trench [Road 10]	16	26-Jan-27	13-Feb-27	10-Aug-26 A	23-Aug-26 A	0.00	6,816.52	6,816.52	0%	100%	149
JDH4-02-007-C	Installation of Duct banks [Road 10]	21	14-Feb-27	14-Mar-27	10-Aug-26 A	23-Aug-26 A	0.00	9,251.02	9,251.02	0%	100%	170
JDH4-02-007-C	Installation of Medium Voltage Cable	14	01-Apr-27	25-Apr-27	10-Aug-26 A	23-Aug-26 A	0.00	114,911.01	114,911.01	0%	100%	206
Medium Voltage Cable Out of Zone		29	07-Mar-27	06-May-27	20-Jun-26 A	13-Oct-26 A	0.00	196,298.15	196,298.15	0%	100%	172
JDH4-02-007-C	Excavation for Trench [Out of Zone]	21	07-Mar-27	03-Apr-27	20-Jun-26 A	03-Oct-26 A	0.00	9,236.12	9,236.12	0%	100%	153
JDH4-02-007-C	Installation of Duct banks [Out of Zone	16	04-Apr-27	21-Apr-27	25-Jul-26 A	07-Oct-26 A	0.00	33,303.68	33,303.68	0%	100%	165
JDH4-02-007-C	Installation of Medium Voltage Cable	13	22-Apr-27	06-May-27	03-Aug-26 A	13-Oct-26 A	0.00	153,758.35	153,758.35	0%	100%	172
Plot Backfilling 2		31	02-Jan-27	06-Feb-27	28-Jun-26 A	02-Nov-26	0.00	2,686,325.19	3,041,122.86	0%	88.33%	82
JDH4-02-007-CI	Plots backfilling Stage 5 [Plots]	11	02-Jan-27	13-Jan-27	28-Jun-26 A	26-Sep-26 A	0.00	1,013,707.62	1,013,707.62	0%	100%	95
JDH4-02-007-CI	Plots backfilling Stage 6 [Plots]	10	14-Jan-27	25-Jan-27	25-Jul-26 A	27-Oct-26	0.00	912,336.86	1,013,707.62	0%	90%	78
JDH4-02-007-CI	Plots backfilling Stage 7 [Plots]	10	26-Jan-27	06-Feb-27	30-Jul-26 A	02-Nov-26	0.00	760,280.72	1,013,707.62	0%	75%	82
Additional Works		77	26-Jan-27	24-Apr-27	15-Apr-26 A	08-Nov-26	0.00	4,403,319.30	4,574,877.19	0%	96.25%	140
JDH4-02-007-CI	Earth Work	21	26-Jan-27	18-Feb-27	15-Apr-26 A	03-Oct-26 A	0.00	1,143,719.30	1,143,719.30	0%	100%	119
JDH4-02-007-CI	Utilities Work	25	20-Feb-27	24-Mar-27	16-May-26 A	17-Sep-26 A	0.00	1,143,719.30	1,143,719.30	0%	100%	157
JDH4-02-007-CI	Electrical Works	25	25-Mar-27	22-Apr-27	28-Jun-26 A	08-Nov-26	0.00	1,086,533.33	1,143,719.30	0%	95%	139
JDH4-02-007-CI	Road Work	25	27-Mar-27	24-Apr-27	16-May-26 A	02-Nov-26	0.00	1,029,347.37	1,143,719.30	0%	90%	145
Testing & Commissioning		128	12-Jul-26	05-May-27	01-Jun-26 A	02-Jan-27	818,633.54	4,338,757.76	5,730,434.78	14.29%	75.71%	102
JDH4-02-007-TC	Test for Potable Water Network	3	09-Nov-26	11-Nov-26	02-Jun-26 A	18-Aug-26 A	0.00	818,633.54	818,633.54	0%	100%	72
JDH4-02-007-TC	Test for TSE Network	3	08-Nov-26	10-Nov-26	10-Jun-26 A	12-Aug-26 A	0.00	818,633.54	818,633.54	0%	100%	76
JDH4-02-007-TC	Test for Sanitary Sewerage	3	12-Jul-26	14-Jul-26	01-Jun-26 A	08-Jul-26 A	818,633.54	818,633.54	818,633.54	100%	100%	5
JDH4-02-007-TC	Test for Stormwater Utilities	3	26-Nov-26	29-Nov-26	09-Jun-26 A	25-Jul-26 A	0.00	818,633.54	818,633.54	0%	100%	108
JDH4-02-007-TC	Test for Electrical Network	3	20-Dec-26	22-Dec-26	08-Sep-26 A	07-Nov-26	0.00	245,590.06	818,633.54	0%	30%	39
JDH4-02-007-TC	Test for Sewage Lift Station	3	03-May-27	05-May-27	17-Jun-26 A	02-Jan-27	0.00	163,726.71	818,633.54	0%	20%	102
JDH4-02-007-TC	Test for Road Works	3	30-Mar-27	01-Apr-27	09-Jun-26 A	07-Nov-26	0.00	654,906.83	818,633.54	0%	80%	121
Project Hand Over & Close-out		71	15-Jul-26	23-May-27	14-Jul-26 A	14-Jan-27	0.00	0.00	0.00	0%	0%	102
As-Built DWGs		71	15-Jul-26	23-May-27	14-Jul-26 A	14-Jan-27	0.00	0.00	0.00	0%	0%	102
As-Built DWGs Submittal		65	15-Jul-26	11-May-27	14-Jul-26 A	07-Jan-27	0.00	0.00	0.00	0%	0%	102
JDH4-02-007-A	As-Built DWGs Submittal for Potable	5	12-Nov-26	17-Nov-26	13-Aug-26 A	19-Aug-26 A	0.00	0.00	0.00	0%	100%	76
JDH4-02-007-A	As-Built DWGs Submittal for TSE Ne	5	11-Nov-26	16-Nov-26	12-Aug-26 A	17-Aug-26 A	0.00	0.00	0.00	0%	100%	77
JDH4-02-007-A	As-Built DWGs Submittal for Sanitary	3	15-Jul-26	18-Jul-26	14-Jul-26 A	12-Aug-26 A	0.00	0.00	0.00	100%	100%	-21
JDH4-02-007-A	As-Built DWGs Submittal for Stormw	5	01-Dec-26	06-Dec-26	06-Aug-26 A	20-Aug-26 A	0.00	0.00	0.00	0%	100%	91
JDH4-02-007-A	As-Built DWGs Submittal for Electric	5	23-Dec-26	28-Dec-26	14-Oct-26 A	12-Nov-26	0.00	0.00	0.00	0%	35%	39
JDH4-02-007-A	As-Built DWGs Submittal for Sewage	5	06-May-27	11-May-27	03-Jan-27	07-Jan-27	0.00	0.00	0.00	0%	0%	102
JDH4-02-007-A	As-Built DWGs Submittal for Road W	5	25-Apr-27	29-Apr-27	14-Oct-26 A	12-Nov-26	0.00	0.00	0.00	0%	35%	140
As-Built DWGs Approval		68	19-Jul-26	23-May-27	13-Aug-26 A	14-Jan-27	0.00	0.00	0.00	0%	0%	102
JDH4-02-007-A	As- Built DWGs Approval for Potable	3	18-Nov-26	21-Nov-26	20-Aug-26 A	05-Sep-26 A	0.00	0.00	0.00	0%	100%	66
JDH4-02-007-A	As- Built DWGs Approval for TSE Ne	6	17-Nov-26	23-Nov-26	18-Aug-26 A	29-Aug-26 A	0.00	0.00	0.00	0%	100%	73
JDH4-02-007-A	As- Built DWGs Approval for Sanitary	4	19-Jul-26	22-Jul-26	13-Aug-26 A	26-Aug-26 A	0.00	0.00	0.00	100%	100%	-29
JDH4-02-007-A	As- Built DWGs Approval for Stormw	6	07-Dec-26	13-Dec-26	20-Aug-26 A	06-Sep-26 A	0.00	0.00	0.00	0%	100%	84
JDH4-02-007-A	As- Built DWGs Approval for Electric	6	29-Dec-26	04-Jan-27	14-Nov-26	19-Nov-26	0.00	0.00	0.00	0%	0%	39
JDH4-02-007-A	As- Built DWGs Approval for Sewage	6	12-May-27	23-May-27	09-Jan-27	14-Jan-27	0.00	0.00	0.00	0%	0%	102
JDH4-02-007-A	As- Built DWGs Approval for Road W	6	01-May-27	06-May-27	14-Nov-26	19-Nov-26	0.00	0.00	0.00	0%	0%	140
Demobilization		35	08-May-27	23-May-27	21-Nov-26	30-Dec-26	0.00	0.00	0.00	0%	0%	115
JDH4-02-007-DI	Demobilization of Manpower	5	08-May-27	12-May-27	21-Nov-26	25-Nov-26	0.00	0.00	0.00	0%	0%	140
JDH4-02-007-DI	Removal of Equipment from Site	5	08-May-27	12-May-27	21-Nov-26	25-Nov-26	0.00	0.00	0.00	0%	0%	140
JDH4-02-007-DI	Site Clean Up	5	08-May-27	12-May-27	21-Nov-26	25-Nov-26	0.00	0.00	0.00	0%	0%	140
JDH4-02-007-DI	Removal of Site Offices and Structure	5	08-May-27	12-May-27	21-Nov-26	25-Nov-26	0.00	0.00	0.00	0%	0%	140
JDH4-02-007-DI	Restoration of Ground Surfaces	5	13-May-27	23-May-27	26-Dec-26	30-Dec-26	0.00	0.00	0.00	0%	0%	115

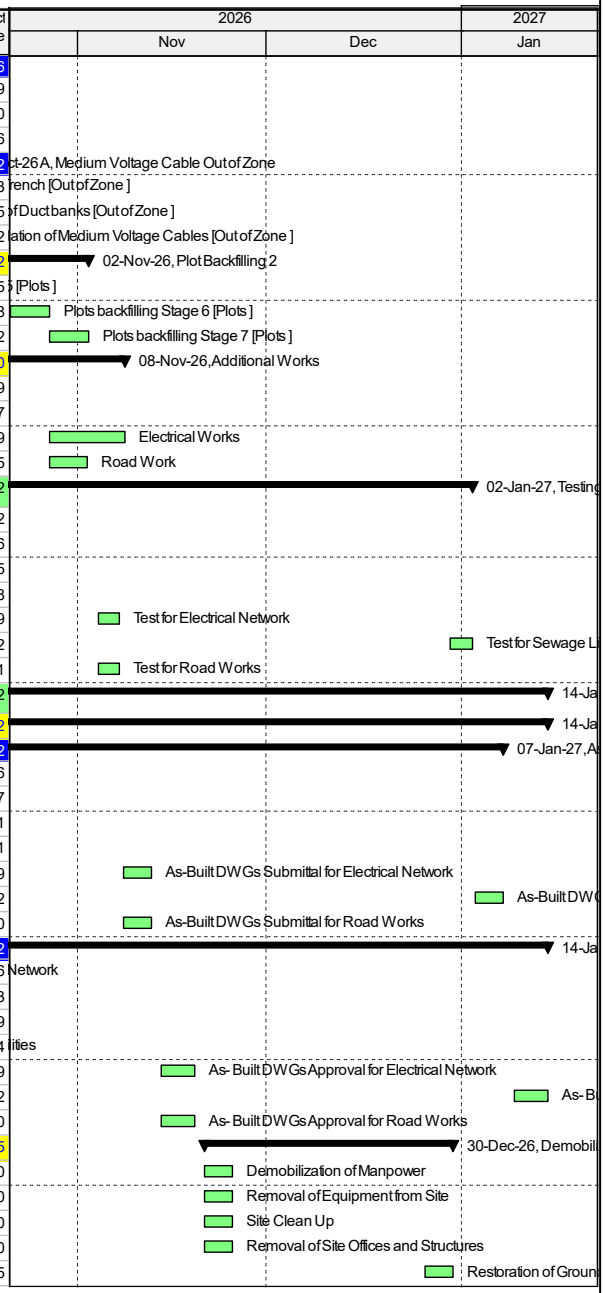

Actual Work | Critical Remaining Work | Remaining Work | Milestone

Date	Revision	Checked	Approved
