
Development of the Technology City in Dharan Project
BL-Update 26-10-2026
WPR UPS LEVEL 5


Activity ID	Activity Name	Original Duration	Start	Finish	Budgeted Total Cost	Planned Value Cost	Earned Value Cost	Actual Total Cost	Schedule % Complete	Performance % Complete
Development of the Technology City in Dhahran Project Recovery -R		3680	06-Jan-26 A	15-Jul-27	93,388,700	35,616,581	23,396,765	22,760,264	38.14%	25.05%
Key Milestones		3680	06-Jan-26 A	15-Jul-27	0	0	0	0	0%	0%
Contractual Milestones		3680	06-Jan-26 A	15-Jul-27	0	0	0	0	0%	0%
MS-CF-EBL	Completion of Execution Plan and Baseline Schedule	0		05-Feb-26 A	0	0	0	0	100%	100%
MS-CF-ENG	Completion of Submitting and Approval of Shopdrawing and Materials	0		22-Nov-26	0	0	0	0	100%	0%
MS-CF-IR	Completion of Construction Works for Irrigation Network	0		12-May-27	0	0	0	0	0%	0%
MS-CF-LO	Completion of Construction Works for Low Voltage Network	0		12-May-27	0	0	0	0	0%	0%
MS-CF-MOB	Completion of Mobilization Works	0		07-Mar-26 A	0	0	0	0	100%	100%
MS-CF-MV	Completion of Construction Works for Medium Voltage Network	0		17-Apr-27	0	0	0	0	0%	0%
MS-CF-PF	Project Completion Date	0		15-Jul-27	0	0	0	0	0%	0%
MS-CF-PW	Completion of Construction Works for Potable Water Network	0		12-May-27	0	0	0	0	0%	0%
MS-CF-RD	Completion of Construction Works for Road Works	0		12-May-27	0	0	0	0	0%	0%
MS-CF-SD	Completion of Construction Works for Storm Drainage Network	0		11-May-27	0	0	0	0	0%	0%
MS-CF-SL	Completion of Construction Works for Street Lighting Network	0		11-May-27	0	0	0	0	0%	0%
MS-CF-SW	Completion of Construction Works for Sewage Network	0		04-Mar-27	0	0	0	0	0%	0%
MS-CF-TE	Completion of Construction Works for Telecom and Light Current Networks	0		12-May-27	0	0	0	0	0%	0%
MS-CF-TSE	Completion of Construction Works for Treated Sewage Effluent Network	0		05-Jun-27	0	0	0	0	0%	0%
MS-CS-PS	Project Commencement Date (Site Handover)	0	06-Jan-26 A		0	0	0	0	100%	100%
MS-MO-10	Completion of Sewage Pump Station	0		23-Jun-27	0	0	0	0	0%	0%
MS-MO-20	Completion of Storm Drainage Ponds	0		05-May-27	0	0	0	0	0%	0%
MS-MO-40	Completion of Control Room	0		12-Jul-27	0	0	0	0	0%	0%
MS-MO-50	Completion of Water Pump Station	0		23-Jun-27	0	0	0	0	0%	0%
MS-MO-60	Completion of Irrigation and Potable Tank	0		20-Jun-27	0	0	0	0	0%	0%
Control Milestones		1936	06-Jan-26 A	26-Oct-26	0	0	0	0	0%	0%
The Employer		1744	03-Feb-26 A	26-Oct-26	0	0	0	0	0%	0%
MS-MM-100	Right of Access and Possession of the Site	0		03-Feb-26 A	0	0	0	0	100%	100%
MS-MM-120	Receipt of Advance Payment for the Project From The Employer	0		26-Oct-26	0	0	0	0	100%	0%
MS-MM-130	Receipt the Site Benchmark Coordinates (Original Point) From The Employer	0		03-Feb-26 A	0	0	0	0	100%	100%
MS-MM-140	Receipt the Site Levels Details From The Employer	0		03-Feb-26 A	0	0	0	0	100%	100%
MS-MM-150	Receipt of Approved Concept Master Plan for the Project From the Employer	0		03-Feb-26 A	0	0	0	0	100%	100%
MS-MM-160	Receipt of Master Plan Approval Letter for the Project From the Employer	0		03-Feb-26 A	0	0	0	0	100%	100%
NOC's		0	06-Jan-26 A	06-Jan-26 A	0	0	0	0	0%	0%
Infrastructure Networks		0	06-Jan-26 A	06-Jan-26 A	0	0	0	0	0%	0%
MS-CS-IR	Receipt of Approval NOC From Relevant Authorities For Irrigation Network	0	06-Jan-26 A		0	0	0	0	100%	100%

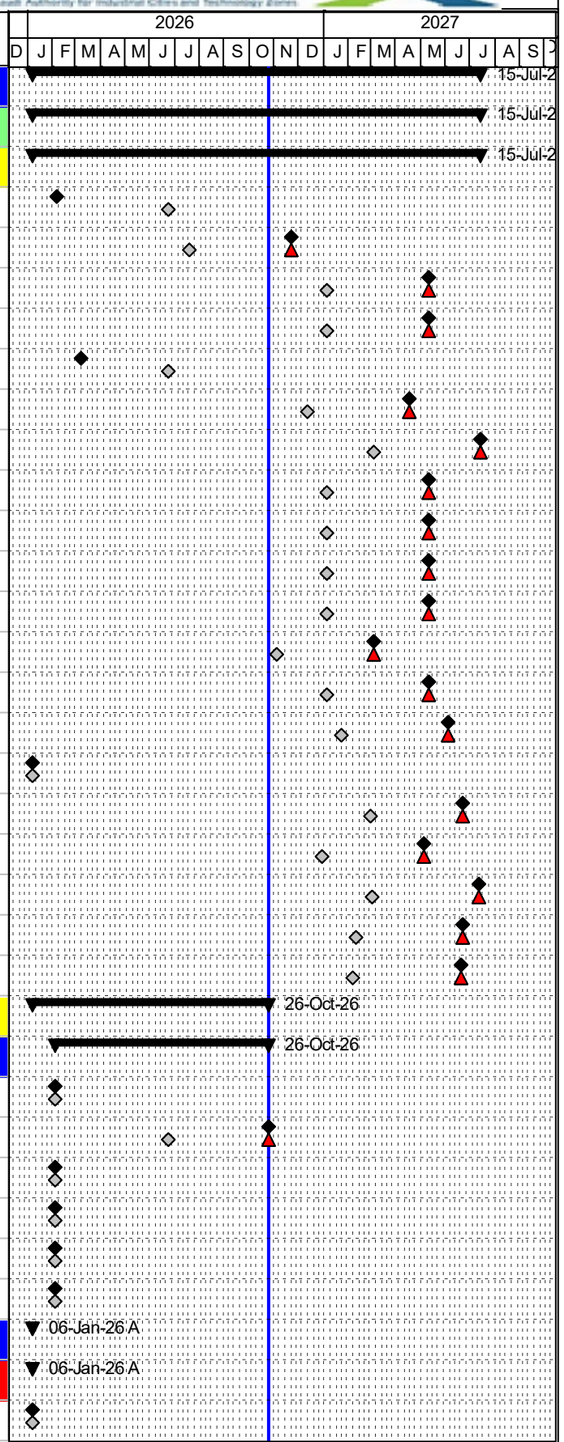

Primary Baseline
Remaining Work
Critical Remaining Work
Actual Work
Baseline Milestone
Milestone
Summary

Date	Revision	Checked	Approved
26-Oct-26	Third Industrial City		


Activity ID	Activity Name	Original Duration	Start	Finish	Budgeted Total Cost	Planned Value Cost	Earned Value Cost	Actual Total Cost	Schedule % Complete	Performance % Complete
MS-CS-LV	Receipt of Approval NOC From Relevant Authorities For Low Voltage Network	0	06-Jan-26 A		0	0	0	0	100%	100%
MS-CS-MV	Receipt of Approval NOC From Relevant Authorities For Medium Voltage Network	0	06-Jan-26 A		0	0	0	0	100%	100%
MS-CS-PW	Receipt of Approval NOC From Relevant Authorities For Potable Water Network	0	06-Jan-26 A		0	0	0	0	100%	100%
MS-CS-RD	Receipt of Approval NOC From Relevant Authorities For Roads Network	0	06-Jan-26 A		0	0	0	0	100%	100%
MS-CS-SD	Receipt of Approval NOC From Relevant Authorities For Storm Network	0	06-Jan-26 A		0	0	0	0	100%	100%
MS-CS-SL	Receipt of Approval NOC From Relevant Authorities For Street Lighting Network	0	06-Jan-26 A		0	0	0	0	100%	100%
MS-CS-SW	Receipt of Approval NOC From Relevant Authorities For Sewage Network	0	06-Jan-26 A		0	0	0	0	100%	100%
MS-CS-TE	Receipt of Approval NOC From Relevant Authorities For Telecom and Light Current	0	06-Jan-26 A		0	0	0	0	100%	100%
MS-CS-TSE	Receipt of Approval NOC From Relevant Authorities For Treated Sewage Effluent	0	06-Jan-26 A		0	0	0	0	100%	100%
Superstructure Works		0	06-Jan-26 A	06-Jan-26 A	0	0	0	0	0%	0%
MS-CS-IR10	Receipt of Approval NOC From Relevant Authorities For Sewage Pump Station	0	06-Jan-26 A		0	0	0	0	100%	100%
MS-CS-LV10	Receipt of Approval NOC From Relevant Authorities For Boundary Fence	0	06-Jan-26 A		0	0	0	0	100%	100%
MS-CS-MV10	Receipt of Approval NOC From Relevant Authorities For Water Pump Station	0	06-Jan-26 A		0	0	0	0	100%	100%
MS-CS-SL10	Receipt of Approval NOC From Relevant Authorities For Storm Drainage Ponds	0	06-Jan-26 A		0	0	0	0	100%	100%
MS-CS-TE10	Receipt of Approval NOC From Relevant Authorities For Storage Tank (TSE)	0	06-Jan-26 A		0	0	0	0	100%	100%
MS-CS-TE20	Receipt of Approval NOC From Relevant Authorities For Control Room	0	06-Jan-26 A		0	0	0	0	100%	100%
MS-CS-TSE10	Receipt of Approval NOC From Relevant Authorities For Gaurd Room	0	06-Jan-26 A		0	0	0	0	100%	100%
Preliminaries and Mobilization Works		632	06-Jan-26 A	11-Apr-26 A	0	0	0	0	0%	0%
Mobilization Works		632	06-Jan-26 A	11-Apr-26 A	0	0	0	0	0%	0%
MOB-10	Clear and Grub for Offices and Access Roads	112	06-Jan-26 A	20-Jan-26 A	0	0	0	0	100%	100%
MOB-20	Project Site Layout Plan Approval	56	21-Jan-26 A	27-Jan-26 A	0	0	0	0	100%	100%
MOB-30	Supply & Install of Temporary Offices for the Project	72	01-Apr-26 A	09-Apr-26 A	0	0	0	0	100%	100%
MOB-40	Construction Project Store	80	01-Apr-26 A	11-Apr-26 A	0	0	0	0	100%	100%
MOB-50	Mobilization of Major Manpower	48	12-Feb-26 A	26-Feb-26 A	0	0	0	0	100%	100%
MOB-60	Mobilization of Major Equipments	48	12-Feb-26 A	07-Mar-26 A	0	0	0	0	100%	100%
MOB-70	Installation Project Sign Board	80	01-Apr-26 A	11-Apr-26 A	0	0	0	0	100%	100%
MOB-80	Construction Site Access Roads	136	28-Jan-26 A	15-Feb-26 A	0	0	0	0	100%	100%
Project Main Documents From The Contractor		224	06-Jan-26 A	05-Feb-26 A	0	0	0	0	0%	0%
PRE-CON-MDC-10	Submission Project Execution Plan	224	06-Jan-26 A	05-Feb-26 A	0	0	0	0	100%	100%
PRE-CON-MDC-20	Submission Project Baseline Schedule	224	06-Jan-26 A	05-Feb-26 A	0	0	0	0	100%	100%
PRE-CON-MDC-30	Submission Project Health & Safety Plan	224	06-Jan-26 A	05-Feb-26 A	0	0	0	0	100%	100%
PRE-CON-MDC-40	Submission Project Quality Control Plan	224	06-Jan-26 A	05-Feb-26 A	0	0	0	0	100%	100%
PRE-CON-MDC-50	Submission Project Surveying Report	224	06-Jan-26 A	05-Feb-26 A	0	0	0	0	100%	100%
PRE-CON-MDC-60	Submission Project Geotechnical Soil Report	224	06-Jan-26 A	05-Feb-26 A	0	0	0	0	100%	100%

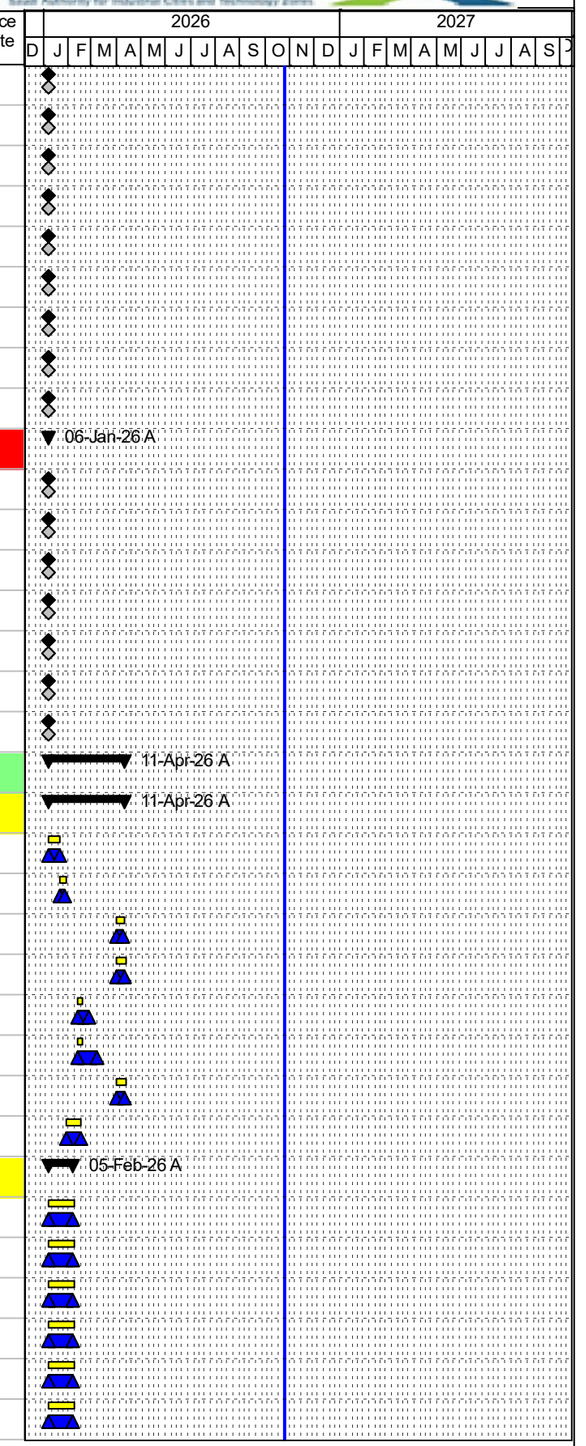

Primary Baseline
Remaining Work
Critical Remaining Work
Actual Work
Baseline Milestone
Milestone
Summary

Date	Revision	Checked	Approved
26-Oct-26	Third Industrial City		


Activity ID	Activity Name	Original Duration	Start	Finish	Budgeted Total Cost	Planned Value Cost	Earned Value Cost	Actual Total Cost	Schedule % Complete	Performance % Complete
PRE-CON-MDC-70	Submission Project Environmental Plan	224	06-Jan-26 A	05-Feb-26 A	0	0	0	0	100%	100%
PRE-CON-MDC-80	Submission Project Organization Chart and Communications Plan	224	06-Jan-26 A	05-Feb-26 A	0	0	0	0	100%	100%
Engineering Works		2128	06-Jan-26 A	22-Nov-26	0	0	0	0	0%	0%
Shop Drawings		216	06-Jan-26 A	04-Feb-26 A	0	0	0	0	0%	0%
Infrastructure Networks		216	06-Jan-26 A	04-Feb-26 A	0	0	0	0	0%	0%
Road Works		216	06-Jan-26 A	04-Feb-26 A	0	0	0	0	0%	0%
General Road Works		168	06-Jan-26 A	28-Jan-26 A	0	0	0	0	0%	0%
ENG-SH-RD-A-100	Approval Shop Drawings for Plan and Profile of Road Works	56	11-Jan-26 A	17-Jan-26 A	0	0	0	0	100%	100%
ENG-SH-RD-A-110	Approval Shop Drawings for Roads Typical Sections and Pavement Details	56	22-Jan-26 A	28-Jan-26 A	0	0	0	0	100%	100%
ENG-SH-RD-S-100	Submission Shop Drawings for Plan and Profile of Road Works	40	06-Jan-26 A	10-Jan-26 A	0	0	0	0	100%	100%
ENG-SH-RD-S-110	Submission Shop Drawings for Roads Typical Sections and Pavement Details	40	18-Jan-26 A	21-Jan-26 A	0	0	0	0	100%	100%
Landscape Works		104	22-Jan-26 A	04-Feb-26 A	0	0	0	0	0%	0%
ENG-SH-HS-A-110	Approval Shop Drawings for Landscape Works	56	29-Jan-26 A	04-Feb-26 A	0	0	0	0	100%	100%
ENG-SH-HS-S-100	Submission Shop Drawings for Landscape Works	56	22-Jan-26 A	28-Jan-26 A	0	0	0	0	100%	100%
Traffic Sign Boards and Road Marking		104	22-Jan-26 A	04-Feb-26 A	0	0	0	0	0%	0%
ENG-SH-MRK-A-110	Approval Shop Drawings for Road Markings	56	29-Jan-26 A	04-Feb-26 A	0	0	0	0	100%	100%
ENG-SH-MRK-S-110	Submission Shop Drawings for Road Markings	56	22-Jan-26 A	28-Jan-26 A	0	0	0	0	100%	100%
ENG-SH-TSB-A-100	Approval Shop Drawings for Traffic Signs Boards	56	29-Jan-26 A	04-Feb-26 A	0	0	0	0	100%	100%
ENG-SH-TSB-S-100	Submission Shop Drawings for Traffic Signs Boards	56	22-Jan-26 A	28-Jan-26 A	0	0	0	0	100%	100%
Storm Drainage Network		104	22-Jan-26 A	04-Feb-26 A	0	0	0	0	0%	0%
Main Line Sections		104	22-Jan-26 A	04-Feb-26 A	0	0	0	0	0%	0%
ENG-SH-SD-ML-A-110	Approval Shop Drawings for Main Line and Manholes of Storm Drainage Network	56	29-Jan-26 A	04-Feb-26 A	0	0	0	0	100%	100%
ENG-SH-SD-ML-S-100	Submission Shop Drawings for Main Line and Manholes of Storm Drainage Network	56	22-Jan-26 A	28-Jan-26 A	0	0	0	0	100%	100%
Catch Basin Sections		104	22-Jan-26 A	04-Feb-26 A	0	0	0	0	0%	0%
ENG-SH-SD-CB-A-110	Approval Shop Drawings for Secondary Line and Catch Basin of Storm Drainage Network	56	29-Jan-26 A	04-Feb-26 A	0	0	0	0	100%	100%
ENG-SH-SD-CB-S-100	Submission Shop Drawings for Secondary Line and Catch Basin of Storm Drainage	56	22-Jan-26 A	28-Jan-26 A	0	0	0	0	100%	100%
Storm Drainage Ponds		56	22-Jan-26 A	28-Jan-26 A	0	0	0	0	0%	0%
ENG-SH-DPO-A-120	Approval Shop Drawings Package for Storm Drainage Ponds	32	26-Jan-26 A	28-Jan-26 A	0	0	0	0	100%	100%
ENG-SH-DPO-S-110	Submission Shop Drawings Package for Storm Drainage Ponds	32	22-Jan-26 A	25-Jan-26 A	0	0	0	0	100%	100%
Sewage Network		104	22-Jan-26 A	04-Feb-26 A	0	0	0	0	0%	0%
Main Line Sections		104	22-Jan-26 A	04-Feb-26 A	0	0	0	0	0%	0%
ENG-SH-SW-ML-A-110	Approval Shop Drawings for Main Line and Manholes of Sewage Network	56	29-Jan-26 A	04-Feb-26 A	0	0	0	0	100%	100%
ENG-SH-SW-ML-S-100	Submission Shop Drawings for Main Line and Manholes of Sewage Network	56	22-Jan-26 A	28-Jan-26 A	0	0	0	0	100%	100%
Treated Sewage Effluent Network		104	22-Jan-26 A	04-Feb-26 A	0	0	0	0	0%	0%

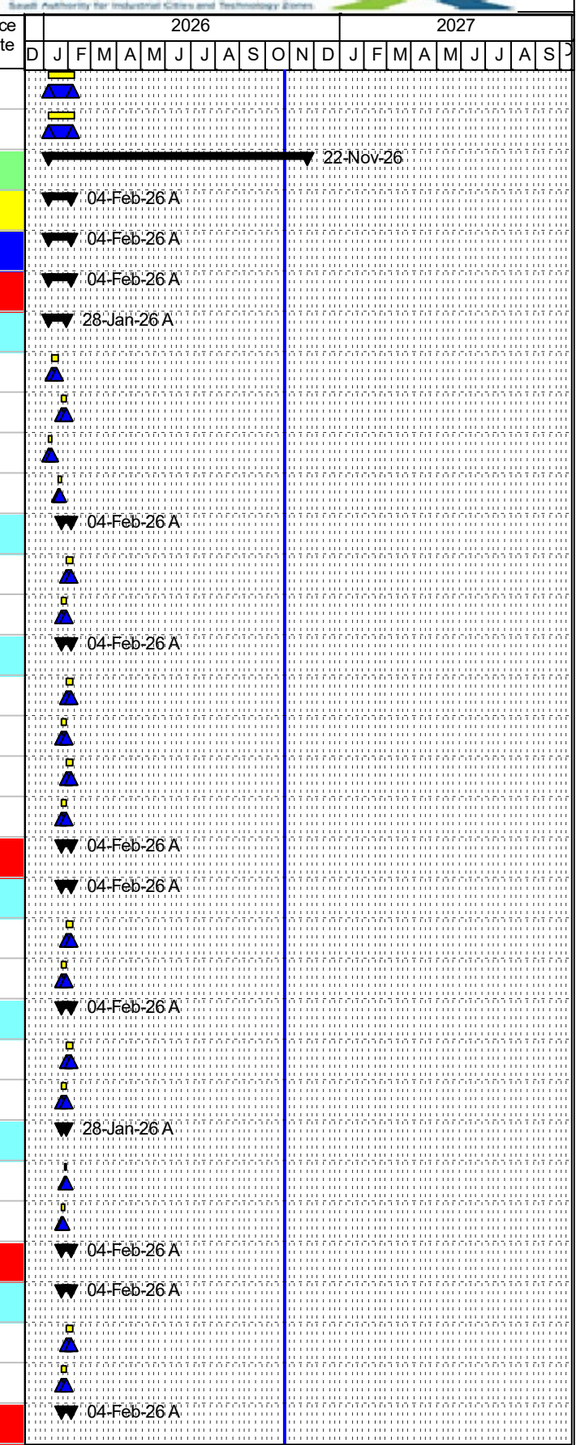

Primary Baseline
Remaining Work
Critical Remaining Work
Actual Work
Baseline Milestone
Milestone
Summary

Date	Revision	Checked	Approved
26-Oct-26	Third Industrial City		


Activity ID	Activity Name	Original Duration	Start	Finish	Budgeted Total Cost	Planned Value Cost	Earned Value Cost	Actual Total Cost	Schedule % Complete	Performance % Complete
ENG-SH-TSE-ML-A-120	Approval Shop Drawings for Main Line Treated Sewage Effluent Network	56	29-Jan-26 A	04-Feb-26 A	0	0	0	0	100%	100%
ENG-SH-TSE-ML-S-110	Submission Shop Drawings for Main Line Treated Sewage Effluent Network	56	22-Jan-26 A	28-Jan-26 A	0	0	0	0	100%	100%
Potable Water Network		104	22-Jan-26 A	04-Feb-26 A	0	0	0	0	0%	0%
Main Line Sections		104	22-Jan-26 A	04-Feb-26 A	0	0	0	0	0%	0%
ENG-SH-PW-ML-A-110	Approval Shop Drawings for Main Line and Valve Chambers of Potable Water Network	56	29-Jan-26 A	04-Feb-26 A	0	0	0	0	100%	100%
ENG-SH-PW-ML-S-100	Submission Shop Drawings for Main Line and Valve Chambers of Potable Water Network	56	22-Jan-26 A	28-Jan-26 A	0	0	0	0	100%	100%
Fire Hydrant		104	22-Jan-26 A	04-Feb-26 A	0	0	0	0	0%	0%
ENG-SH-PW-FH-A-110	Approval Shop Drawings for Fire Hydrant Network	56	29-Jan-26 A	04-Feb-26 A	0	0	0	0	100%	100%
ENG-SH-PW-FH-S-100	Submission Shop Drawings for Fire Hydrant Network	56	22-Jan-26 A	28-Jan-26 A	0	0	0	0	100%	100%
Irrigation Network		104	22-Jan-26 A	04-Feb-26 A	0	0	0	0	0%	0%
Main Line Sections		104	22-Jan-26 A	04-Feb-26 A	0	0	0	0	0%	0%
ENG-SH-IR-ML-A-110	Approval Shop Drawings for Main Line and Valves & Bulbblers and Sprinklers of Irrigation	56	29-Jan-26 A	04-Feb-26 A	0	0	0	0	100%	100%
ENG-SH-IR-ML-S-100	Submission Shop Drawings for Main Line and Valves & Bulbblers and Sprinklers of Irrigation	56	22-Jan-26 A	28-Jan-26 A	0	0	0	0	100%	100%
Medium Voltage Network		104	22-Jan-26 A	04-Feb-26 A	0	0	0	0	0%	0%
ENG-SH-MV-A-110	Approval Shop Drawings for Medium Voltage Network	56	29-Jan-26 A	04-Feb-26 A	0	0	0	0	100%	100%
ENG-SH-MV-S-100	Submission Shop Drawings for Medium Voltage Network	56	22-Jan-26 A	28-Jan-26 A	0	0	0	0	100%	100%
Low Voltage Network		104	22-Jan-26 A	04-Feb-26 A	0	0	0	0	0%	0%
ENG-SH-LV-A-120	Approval Shop Drawings for Low Voltage Network	56	29-Jan-26 A	04-Feb-26 A	0	0	0	0	100%	100%
ENG-SH-LV-S-110	Submission Shop Drawings for Low Voltage Network	56	22-Jan-26 A	28-Jan-26 A	0	0	0	0	100%	100%
Street Lighting Network		104	22-Jan-26 A	04-Feb-26 A	0	0	0	0	0%	0%
ENG-SH-SL-A-110	Approval Shop Drawings for Street Lighting Network	56	29-Jan-26 A	04-Feb-26 A	0	0	0	0	100%	100%
ENG-SH-SL-S-100	Submission Shop Drawings for Street Lighting Network	56	22-Jan-26 A	28-Jan-26 A	0	0	0	0	100%	100%
Telecom Network		104	22-Jan-26 A	04-Feb-26 A	0	0	0	0	0%	0%
ENG-SH-CTV-A-110	Approval Shop Drawings for CCTV and Telephone Complete Systems	56	29-Jan-26 A	04-Feb-26 A	0	0	0	0	100%	100%
ENG-SH-CTV-S-100	Submission Shop Drawings for CCTV and Telephone Complete Systems	56	22-Jan-26 A	28-Jan-26 A	0	0	0	0	100%	100%
ENG-SH-MSN-A-120	Approval Shop Drawings for MSN and Access Control Systems	56	22-Jan-26 A	28-Jan-26 A	0	0	0	0	100%	100%
ENG-SH-MSN-S-110	Submission Shop Drawings for MSN and Access Control Systems	56	22-Jan-26 A	28-Jan-26 A	0	0	0	0	100%	100%
ENG-SH-TE-A-110	Approval Shop Drawings for Telecom Network	56	29-Jan-26 A	04-Feb-26 A	0	0	0	0	100%	100%
ENG-SH-TE-S-100	Submission Shop Drawings for Telecom Network	56	22-Jan-26 A	28-Jan-26 A	0	0	0	0	100%	100%
Superstructure Works		104	22-Jan-26 A	04-Feb-26 A	0	0	0	0	0%	0%
Water Pump Station		104	22-Jan-26 A	04-Feb-26 A	0	0	0	0	0%	0%
ENG-SH-LS-A-170	Approval Shop Drawings Package for Water Pump Station	56	29-Jan-26 A	04-Feb-26 A	0	0	0	0	100%	100%
ENG-SH-LS-S-160	Submission Shop Drawings Package for Water Pump Station	56	22-Jan-26 A	28-Jan-26 A	0	0	0	0	100%	100%
Storage Tank (TSE)		104	22-Jan-26 A	04-Feb-26 A	0	0	0	0	0%	0%

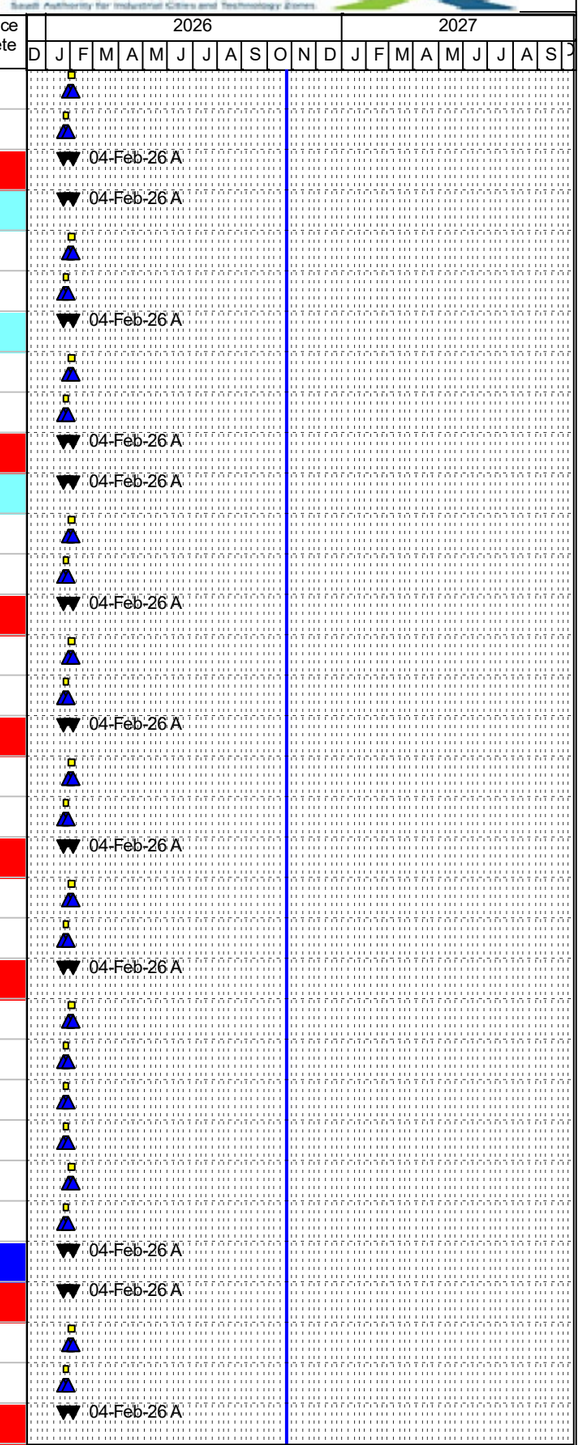

Primary Baseline
Remaining Work
Critical Remaining Work
Actual Work
Baseline Milestone
Milestone
Summary

Date	Revision	Checked	Approved
26-Oct-26	Third Industrial City		


Activity ID	Activity Name	Original Duration	Start	Finish	Budgeted Total Cost	Planned Value Cost	Earned Value Cost	Actual Total Cost	Schedule % Complete	Performance % Complete
ENG-SH-ST-A-180	Approval Shop Drawings Package for Storage Tank TSE	56	29-Jan-26 A	04-Feb-26 A	0	0	0	0	100%	100%
ENG-SH-ST-S-170	Submission Shop Drawings Package for Storage Tank TSE	56	22-Jan-26 A	28-Jan-26 A	0	0	0	0	100%	100%
Control Room		104	22-Jan-26 A	04-Feb-26 A	0	0	0	0	0%	0%
ENG-SH-ST-A-190	Approval Shop Drawings Package for Control Room	56	29-Jan-26 A	04-Feb-26 A	0	0	0	0	100%	100%
ENG-SH-ST-S-180	Submission Shop Drawings Package for Control Room	56	22-Jan-26 A	28-Jan-26 A	0	0	0	0	100%	100%
Sewage Pump Stations		104	22-Jan-26 A	04-Feb-26 A	0	0	0	0	0%	0%
ENG-SH-SPS-A-160	Approval Shop Drawings Package for Sewage Pump Station	56	29-Jan-26 A	04-Feb-26 A	0	0	0	0	100%	100%
ENG-SH-SPS-S-150	Submission Shop Drawings Package for Sewage Pump Station	56	22-Jan-26 A	28-Jan-26 A	0	0	0	0	100%	100%
Gaurd Room		104	22-Jan-26 A	04-Feb-26 A	0	0	0	0	0%	0%
ENG-SH-GR-A-190	Approval Shop Drawings Package for Gaurd Room	56	29-Jan-26 A	04-Feb-26 A	0	0	0	0	100%	100%
ENG-SH-GR-S-180	Submission Shop Drawings Package for Gaurd Room	56	22-Jan-26 A	28-Jan-26 A	0	0	0	0	100%	100%
Boundary Fence		104	22-Jan-26 A	04-Feb-26 A	0	0	0	0	0%	0%
ENG-SH-GR-A-200	Approval Shop Drawings Package for Boundary Fence	56	29-Jan-26 A	04-Feb-26 A	0	0	0	0	100%	100%
ENG-SH-GR-S-190	Submission Shop Drawings Package for Boundary Fence	56	22-Jan-26 A	28-Jan-26 A	0	0	0	0	100%	100%
Method Statements		104	18-Jan-26 A	31-Jan-26 A	0	0	0	0	0%	0%
Infrastructure Networks		104	18-Jan-26 A	31-Jan-26 A	0	0	0	0	0%	0%
Storm Drainage Network		56	25-Jan-26 A	31-Jan-26 A	0	0	0	0	0%	0%
Main Line Sections		40	25-Jan-26 A	28-Jan-26 A	0	0	0	0	0%	0%
ENG-MS-SD-ML-A-110	Approval Method Statement for Main Line of Storm Drainage Network	32	26-Jan-26 A	28-Jan-26 A	0	0	0	0	100%	100%
ENG-MS-SD-ML-S-100	Submission Method Statement for Main Line of Storm Drainage Network	16	25-Jan-26 A	25-Jan-26 A	0	0	0	0	100%	100%
Catch Basin Sections		56	25-Jan-26 A	31-Jan-26 A	0	0	0	0	0%	0%
ENG-MS-SD-CB-A-110	Approval Method Statement for Catch Basin of Storm Drainage Network	32	28-Jan-26 A	31-Jan-26 A	0	0	0	0	100%	100%
ENG-MS-SD-CB-S-100	Submission Method Statement for Catch Basin of Storm Drainage Network	32	25-Jan-26 A	27-Jan-26 A	0	0	0	0	100%	100%
Storm Drainage Ponds		56	25-Jan-26 A	31-Jan-26 A	0	0	0	0	0%	0%
ENG-MS-DPO-A-130	Approval Method Statement Package for Storm Drainage Ponds	32	28-Jan-26 A	31-Jan-26 A	0	0	0	0	100%	100%
ENG-MS-DPO-S-120	Submission Method Statement Package for Storm Drainage Ponds	32	25-Jan-26 A	27-Jan-26 A	0	0	0	0	100%	100%
Sewage Network		56	25-Jan-26 A	31-Jan-26 A	0	0	0	0	0%	0%
Main Line Sections		56	25-Jan-26 A	31-Jan-26 A	0	0	0	0	0%	0%
ENG-MS-SW-ML-A-110	Approval Method Statement for Main Line of Sewage Network	32	28-Jan-26 A	31-Jan-26 A	0	0	0	0	100%	100%
ENG-MS-SW-ML-S-100	Submission Method Statement for Main Line of Sewage Network	32	25-Jan-26 A	27-Jan-26 A	0	0	0	0	100%	100%
Treated Sewage Effluent Network		56	25-Jan-26 A	31-Jan-26 A	0	0	0	0	0%	0%
ENG-MS-TSE-ML-A-120	Approval Method Statement for Main Line of Treated Sewage Effluent Network	32	28-Jan-26 A	31-Jan-26 A	0	0	0	0	100%	100%
ENG-MS-TSE-ML-S-110	Submission Method Statement for Main Line of Treated Sewage Effluent Network	32	25-Jan-26 A	27-Jan-26 A	0	0	0	0	100%	100%
Potable Water Network		56	25-Jan-26 A	31-Jan-26 A	0	0	0	0	0%	0%

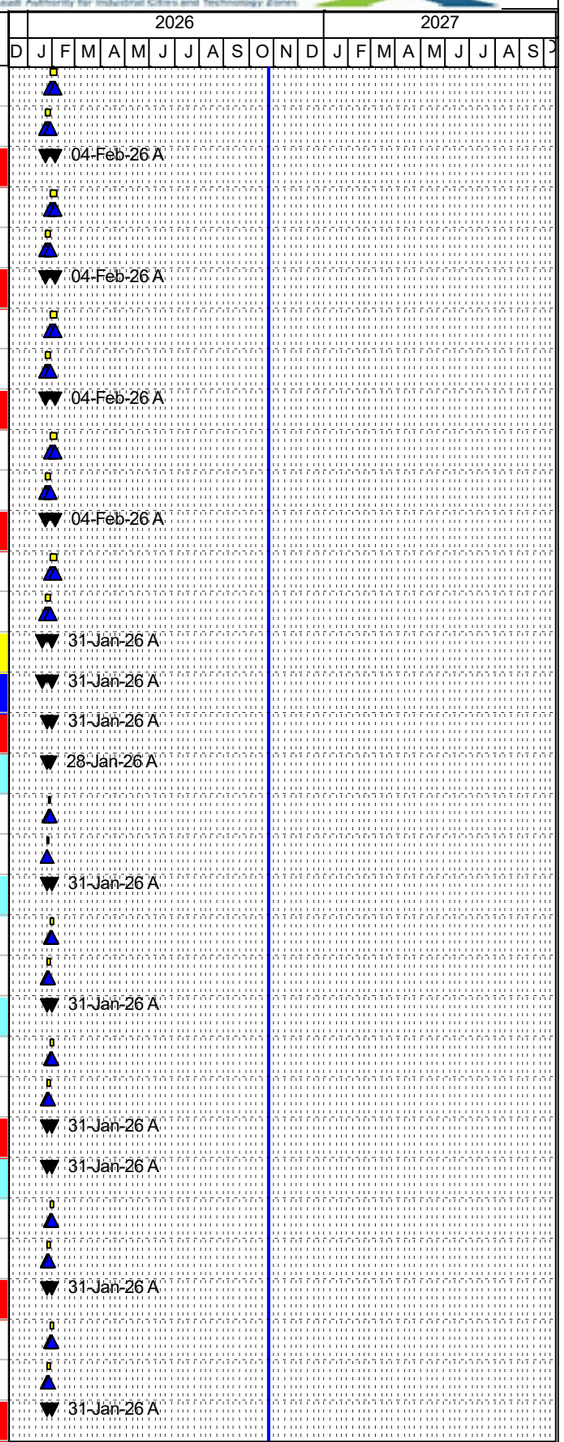

Primary Baseline
Remaining Work
Critical Remaining Work
Actual Work
Baseline Milestone
Milestone
Summary

Date	Revision	Checked	Approved
26-Oct-26	Third Industrial City		


Activity ID	Activity Name	Original Duration	Start	Finish	Budgeted Total Cost	Planned Value Cost	Earned Value Cost	Actual Total Cost	Schedule % Complete	Performance % Complete
Main Line Sections		56	25-Jan-26 A	31-Jan-26 A	0	0	0	0	0%	0%
ENG-MS-PW-ML-A-110	Approval Method Statement for Main Line of Potable Water Network	32	28-Jan-26 A	31-Jan-26 A	0	0	0	0	100%	100%
ENG-MS-PW-ML-S-100	Submission Method Statement for Main Line of Potable Water Network	32	25-Jan-26 A	27-Jan-26 A	0	0	0	0	100%	100%
Irrigation Network		56	25-Jan-26 A	31-Jan-26 A	0	0	0	0	0%	0%
Main Line Sections		56	25-Jan-26 A	31-Jan-26 A	0	0	0	0	0%	0%
ENG-MS-IR-ML-A-110	Approval Method Statement for Main Line of Irrigation Network	32	28-Jan-26 A	31-Jan-26 A	0	0	0	0	100%	100%
ENG-MS-IR-ML-S-100	Submission Method Statement for Main Line of Irrigation Network	32	25-Jan-26 A	27-Jan-26 A	0	0	0	0	100%	100%
Medium Voltage Network		56	25-Jan-26 A	31-Jan-26 A	0	0	0	0	0%	0%
ENG-MS-MV-A-110	Approval Method Statement for Medium Voltage Network	32	28-Jan-26 A	31-Jan-26 A	0	0	0	0	100%	100%
ENG-MS-MV-S-100	Submission Method Statement for Medium Voltage Network	32	25-Jan-26 A	27-Jan-26 A	0	0	0	0	100%	100%
Low Voltage Network		56	25-Jan-26 A	31-Jan-26 A	0	0	0	0	0%	0%
ENG-MS-MV-A-120	Approval Method Statement for Low Voltage Network	32	28-Jan-26 A	31-Jan-26 A	0	0	0	0	100%	100%
ENG-MS-MV-S-110	Submission Method Statement for Low Voltage Network	32	25-Jan-26 A	27-Jan-26 A	0	0	0	0	100%	100%
Street Lighting Network		56	25-Jan-26 A	31-Jan-26 A	0	0	0	0	0%	0%
ENG-MS-SL-A-110	Approval Method Statement for Street Lighting Network	32	28-Jan-26 A	31-Jan-26 A	0	0	0	0	100%	100%
ENG-MS-SL-S-100	Submission Method Statement for Street Lighting Network	32	25-Jan-26 A	27-Jan-26 A	0	0	0	0	100%	100%
Telecom Network		56	25-Jan-26 A	31-Jan-26 A	0	0	0	0	0%	0%
ENG-MS-CTV-A-110	Approval Method Statement for CCTV, Telephone, MSN, and Access Control	32	28-Jan-26 A	31-Jan-26 A	0	0	0	0	100%	100%
ENG-MS-CTV-S-100	Submission Method Statement for CCTV, Telephone, MSN, and Access Control	32	25-Jan-26 A	27-Jan-26 A	0	0	0	0	100%	100%
ENG-MS-TE-A-110	Approval Method Statement for Telecom Network	32	28-Jan-26 A	31-Jan-26 A	0	0	0	0	100%	100%
ENG-MS-TE-S-100	Submission Method Statement for Telecom Network	32	25-Jan-26 A	27-Jan-26 A	0	0	0	0	100%	100%
Road Works		88	18-Jan-26 A	28-Jan-26 A	0	0	0	0	0%	0%
General Road Works		88	18-Jan-26 A	28-Jan-26 A	0	0	0	0	0%	0%
ENG-MS-RD-A-10	Approval Method Statement for Plan and Profile of Road Works	32	21-Jan-26 A	24-Jan-26 A	0	0	0	0	100%	100%
ENG-MS-RD-A-20	Approval Method Statement for Roads Typical Sections and Pavement Details	32	26-Jan-26 A	28-Jan-26 A	0	0	0	0	100%	100%
ENG-MS-RD-A-30	Approval Method Statement of Extraover for Pedestrian ramps	32	21-Jan-26 A	24-Jan-26 A	0	0	0	0	100%	100%
ENG-MS-RD-A-40	Approval Method Statement for Intersections of Road Works	32	21-Jan-26 A	24-Jan-26 A	0	0	0	0	100%	100%
ENG-MS-RD-S-10	Submission Method Statement for Plan and Profile of Road Works	32	18-Jan-26 A	20-Jan-26 A	0	0	0	0	100%	100%
ENG-MS-RD-S-20	Submission Method Statement for Roads Typical Sections and Pavement Details	32	22-Jan-26 A	25-Jan-26 A	0	0	0	0	100%	100%
ENG-MS-RD-S-30	Submission Method Statement of Extraover for Pedestrian ramps	32	18-Jan-26 A	20-Jan-26 A	0	0	0	0	100%	100%
ENG-MS-RD-S-40	Submission Method Statement for Intersections of Road Works	32	18-Jan-26 A	20-Jan-26 A	0	0	0	0	100%	100%
Landscape Works		56	22-Jan-26 A	28-Jan-26 A	0	0	0	0	0%	0%
ENG-MS-HS-A-10	Approval Method Statement for Landscaping Works	32	26-Jan-26 A	28-Jan-26 A	0	0	0	0	100%	100%
ENG-MS-HS-S-10	Submission Method Statement for Landscaping Works	32	22-Jan-26 A	25-Jan-26 A	0	0	0	0	100%	100%

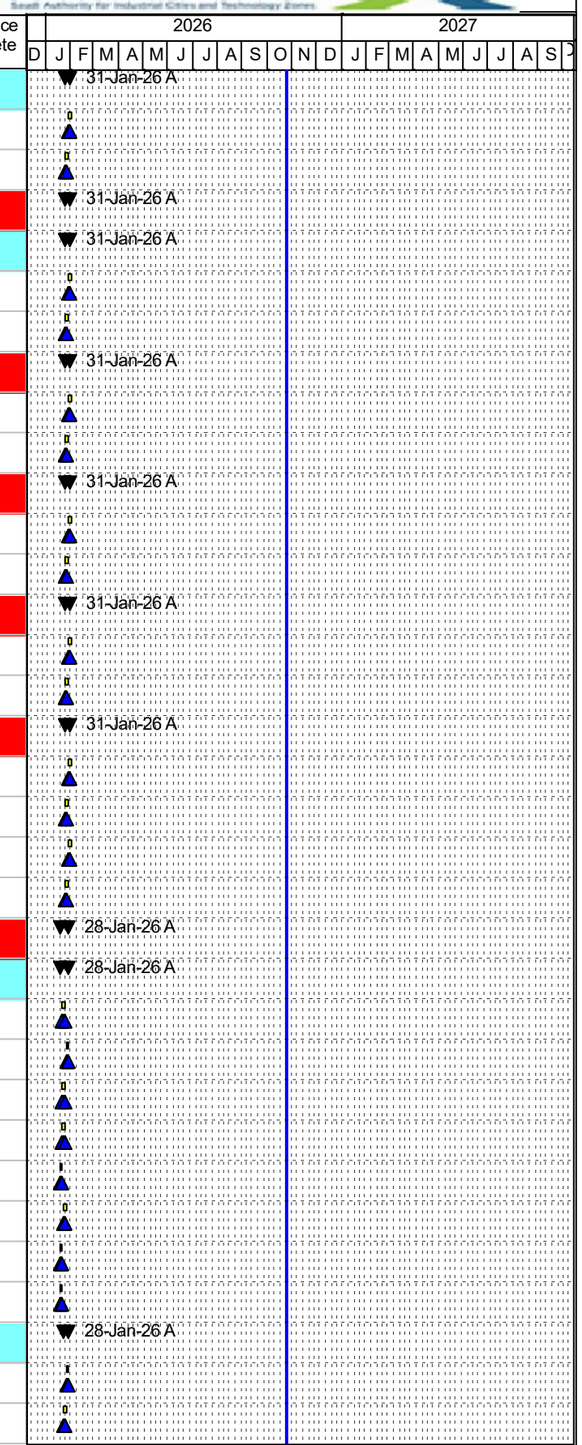

Primary Baseline
Remaining Work
Critical Remaining Work
Actual Work
Baseline Milestone
Milestone
Summary

Date	Revision	Checked	Approved
26-Oct-26	Third Industrial City		


Activity ID	Activity Name	Original Duration	Start	Finish	Budgeted Total Cost	Planned Value Cost	Earned Value Cost	Actual Total Cost	Schedule % Complete	Performance % Complete
Traffic Sign Boards and Road Marking		56	22-Jan-26 A	28-Jan-26 A	0	0	0	0	0%	0%
ENG-MS-MRK-A-10	Approval Method Statement for Roads Markings	32	26-Jan-26 A	28-Jan-26 A	0	0	0	0	100%	100%
ENG-MS-MRK-S-10	Submission Method Statement for Roads Markings	32	22-Jan-26 A	25-Jan-26 A	0	0	0	0	100%	100%
ENG-MS-TSB-A-10	Approval Method Statement for Traffic Signs Boards	32	26-Jan-26 A	28-Jan-26 A	0	0	0	0	100%	100%
ENG-MS-TSB-S-10	Submission Method Statement for Traffic Signs Boards	32	22-Jan-26 A	25-Jan-26 A	0	0	0	0	100%	100%
Superstructure Works		56	25-Jan-26 A	31-Jan-26 A	0	0	0	0	0%	0%
Water Pump Station		56	25-Jan-26 A	31-Jan-26 A	0	0	0	0	0%	0%
ENG-MS-LS-A-180	Approval Method Statement Package for Water Pump Station	32	28-Jan-26 A	31-Jan-26 A	0	0	0	0	100%	100%
ENG-MS-LS-S-170	Submission Method Statement Package for Water Pump Station	32	25-Jan-26 A	27-Jan-26 A	0	0	0	0	100%	100%
Storage Tank (TSE)		56	25-Jan-26 A	31-Jan-26 A	0	0	0	0	0%	0%
ENG-MS-ST-A-190	Approval Method Statement Package for Storage Tank TSE	32	28-Jan-26 A	31-Jan-26 A	0	0	0	0	100%	100%
ENG-MS-ST-S-180	Submission Method Statement Package for Storage Tank TSE	32	25-Jan-26 A	27-Jan-26 A	0	0	0	0	100%	100%
Control Room		56	25-Jan-26 A	31-Jan-26 A	0	0	0	0	0%	0%
ENG-MS-ST-A-200	Approval Method Statement Package for Control Room	32	28-Jan-26 A	31-Jan-26 A	0	0	0	0	100%	100%
ENG-MS-ST-S-190	Submission Method Statement Package for Control Room	32	25-Jan-26 A	27-Jan-26 A	0	0	0	0	100%	100%
Sewage Pump Stations		56	25-Jan-26 A	31-Jan-26 A	0	0	0	0	0%	0%
ENG-MS-SPS-A-170	Approval Method Statement Package for Sewage Pump Station	32	28-Jan-26 A	31-Jan-26 A	0	0	0	0	100%	100%
ENG-MS-SPS-S-160	Submission Method Statement Package for Sewage Pump Station	32	25-Jan-26 A	27-Jan-26 A	0	0	0	0	100%	100%
Gaurd Room		56	25-Jan-26 A	31-Jan-26 A	0	0	0	0	0%	0%
ENG-MS-GR-A-210	Approval Method Statement Package for Gaurd Room	32	28-Jan-26 A	31-Jan-26 A	0	0	0	0	100%	100%
ENG-MS-GR-S-200	Submission Method Statement Package for Gaurd Room	32	25-Jan-26 A	27-Jan-26 A	0	0	0	0	100%	100%
Boundary Fence		56	25-Jan-26 A	31-Jan-26 A	0	0	0	0	0%	0%
ENG-MS-GR-A-220	Approval Method Statement Package for Boundary Fence	32	28-Jan-26 A	31-Jan-26 A	0	0	0	0	100%	100%
ENG-MS-GR-S-210	Submission Method Statement Package for Boundary Fence	32	25-Jan-26 A	27-Jan-26 A	0	0	0	0	100%	100%
Material Submittals and Approvals		2128	06-Jan-26 A	22-Nov-26	0	0	0	0	0%	0%
Short Lead Time Items		992	06-Jan-26 A	13-Jun-26 A	0	0	0	0	0%	0%
Infrastructure Networks		184	06-Jan-26 A	31-Jan-26 A	0	0	0	0	0%	0%
Storm Drainage Network		96	06-Jan-26 A	19-Jan-26 A	0	0	0	0	0%	0%
Submission of Material		56	06-Jan-26 A	12-Jan-26 A	0	0	0	0	0%	0%
Main Line Sections		56	06-Jan-26 A	12-Jan-26 A	0	0	0	0	0%	0%
ENG-MT-SD-ML-S-100	Material Submittal for Manholes of Storm Drainage Network	56	06-Jan-26 A	12-Jan-26 A	0	0	0	0	100%	100%
ENG-MT-SD-ML-S-110	Material Submittal for Main Line Pipes of Storm Drainage Network	56	06-Jan-26 A	12-Jan-26 A	0	0	0	0	100%	100%
Catch Basin Sections		56	06-Jan-26 A	12-Jan-26 A	0	0	0	0	0%	0%
ENG-MT-SD-CB-S-100	Material Submittal for Catch Basins of Storm Drainage Network	56	06-Jan-26 A	12-Jan-26 A	0	0	0	0	100%	100%

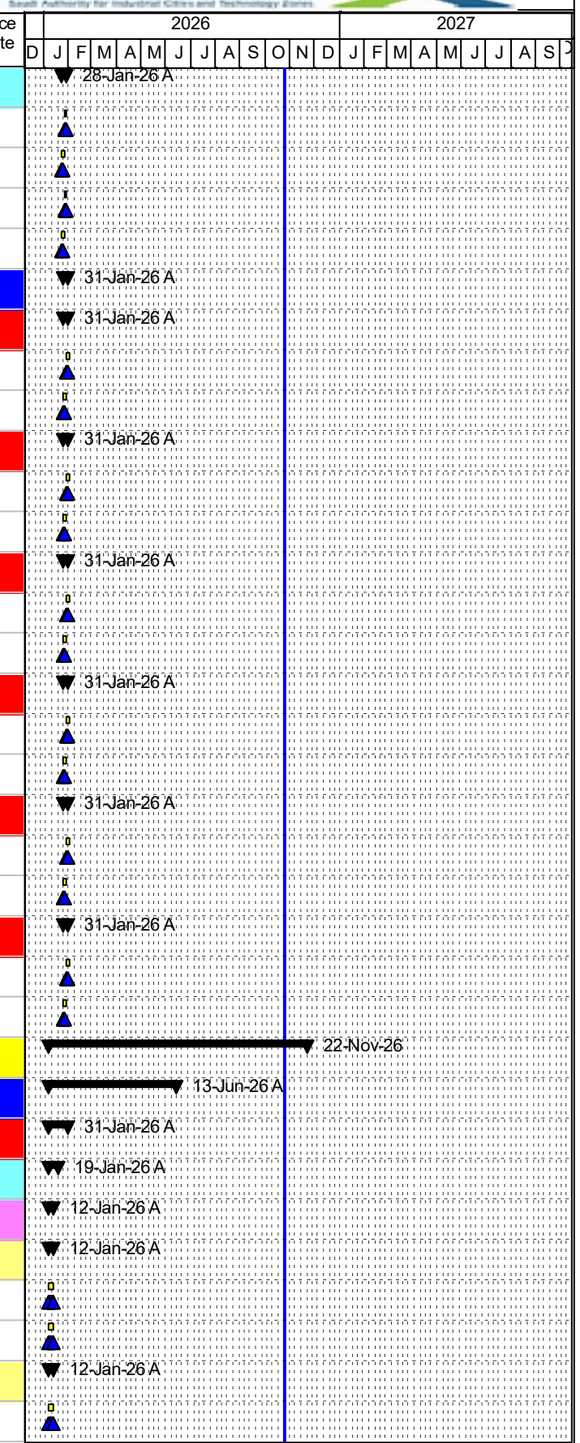

Primary Baseline | Actual Work | Summary
Remaining Work | Baseline Milestone
Critical Remaining Work | Milestone

Date	Revision	Checked	Approved
26-Oct-26	Third Industrial City		


Activity ID	Activity Name	Original Duration	Start	Finish	Budgeted Total Cost	Planned Value Cost	Earned Value Cost	Actual Total Cost	Schedule % Complete	Performance % Complete
ENG-MT-SD-CB-S-110	Material Submittal for Catch Basin Pipes of Storm Drainage Network	56	06-Jan-26 A	12-Jan-26 A	0	0	0	0	100%	100%
Storm Drainage Pond		56	06-Jan-26 A	12-Jan-26 A	0	0	0	0	0%	0%
ENG-MT-DPO-CV-S-100	Material Submittal for Materials of Storm Drainage Ponds	56	06-Jan-26 A	12-Jan-26 A	0	0	0	0	100%	100%
Testing and Finishes		56	06-Jan-26 A	12-Jan-26 A	0	0	0	0	0%	0%
ENG-MT-SD-TF-S-100	Material Submittal for Manhole Covers of Storm Drainage Network	56	06-Jan-26 A	12-Jan-26 A	0	0	0	0	100%	100%
ENG-MT-SD-TF-S-110	Material Submittal for Catch Basin Covers of Storm Drainage Network	56	06-Jan-26 A	12-Jan-26 A	0	0	0	0	100%	100%
Approval of Material		48	13-Jan-26 A	19-Jan-26 A	0	0	0	0	0%	0%
Main Line Sections		48	13-Jan-26 A	19-Jan-26 A	0	0	0	0	0%	0%
ENG-MT-SD-ML-A-100	Material Approval for Manholes of Storm Drainage Network	48	13-Jan-26 A	19-Jan-26 A	0	0	0	0	100%	100%
ENG-MT-SD-ML-A-110	Material Approval for Main Line Pipes of Storm Drainage Network	48	13-Jan-26 A	19-Jan-26 A	0	0	0	0	100%	100%
Catch Basin Sections		48	13-Jan-26 A	19-Jan-26 A	0	0	0	0	0%	0%
ENG-MT-SD-CB-A-100	Material Approval for Catch Basins of Storm Drainage Network	48	13-Jan-26 A	19-Jan-26 A	0	0	0	0	100%	100%
ENG-MT-SD-CB-A-110	Material Approval for Catch Basin Pipes of Storm Drainage Network	48	13-Jan-26 A	19-Jan-26 A	0	0	0	0	100%	100%
Storm Drainage Pond		48	13-Jan-26 A	19-Jan-26 A	0	0	0	0	0%	0%
ENG-MT-DPO-CV-A-110	Material Approval for Materials of Storm Drainage Ponds	48	13-Jan-26 A	19-Jan-26 A	0	0	0	0	100%	100%
Testing and Finishes		48	13-Jan-26 A	19-Jan-26 A	0	0	0	0	0%	0%
ENG-MT-SD-TF-A-100	Material Approval for Manhole Covers of Storm Drainage Network	48	13-Jan-26 A	19-Jan-26 A	0	0	0	0	100%	100%
ENG-MT-SD-TF-A-110	Material Approval for Catch Basin Covers of Storm Drainage Network	48	13-Jan-26 A	19-Jan-26 A	0	0	0	0	100%	100%
Sewage Network		104	06-Jan-26 A	19-Jan-26 A	0	0	0	0	0%	0%
Submission of Material		56	06-Jan-26 A	12-Jan-26 A	0	0	0	0	0%	0%
Main Line Sections		56	06-Jan-26 A	12-Jan-26 A	0	0	0	0	0%	0%
ENG-MT-SW-ML-S-100	Material Submittal for Manholes of Sewage Network	56	06-Jan-26 A	12-Jan-26 A	0	0	0	0	100%	100%
ENG-MT-SW-ML-S-110	Material Submittal for Main Line Pipes of Sewage Network	56	06-Jan-26 A	12-Jan-26 A	0	0	0	0	100%	100%
Testing and Finishes		56	06-Jan-26 A	12-Jan-26 A	0	0	0	0	0%	0%
ENG-MT-SW-TF-S-100	Material Submittal for Manhole Covers of Sewage Network	56	06-Jan-26 A	12-Jan-26 A	0	0	0	0	100%	100%
Approval of Material		56	13-Jan-26 A	19-Jan-26 A	0	0	0	0	0%	0%
Main Line Sections		56	13-Jan-26 A	19-Jan-26 A	0	0	0	0	0%	0%
ENG-MT-SW-ML-A-100	Material Approval for Manholes of Sewage Network	48	13-Jan-26 A	19-Jan-26 A	0	0	0	0	100%	100%
ENG-MT-SW-ML-A-110	Material Approval for Main Line Pipes of Sewage Network	56	13-Jan-26 A	19-Jan-26 A	0	0	0	0	100%	100%
Testing and Finishes		48	13-Jan-26 A	19-Jan-26 A	0	0	0	0	0%	0%
ENG-MT-SW-TF-A-100	Material Approval for Manhole Covers of Sewage Network	48	13-Jan-26 A	19-Jan-26 A	0	0	0	0	100%	100%
Treated Sewage Effluent (Tse)		96	06-Jan-26 A	19-Jan-26 A	0	0	0	0	0%	0%
Submission of Material		56	06-Jan-26 A	12-Jan-26 A	0	0	0	0	0%	0%
ENG-MT-IR-ML-S-120	Material Submittal for Materials of Treated Sewage Effluent (TSE)	56	06-Jan-26 A	12-Jan-26 A	0	0	0	0	100%	100%

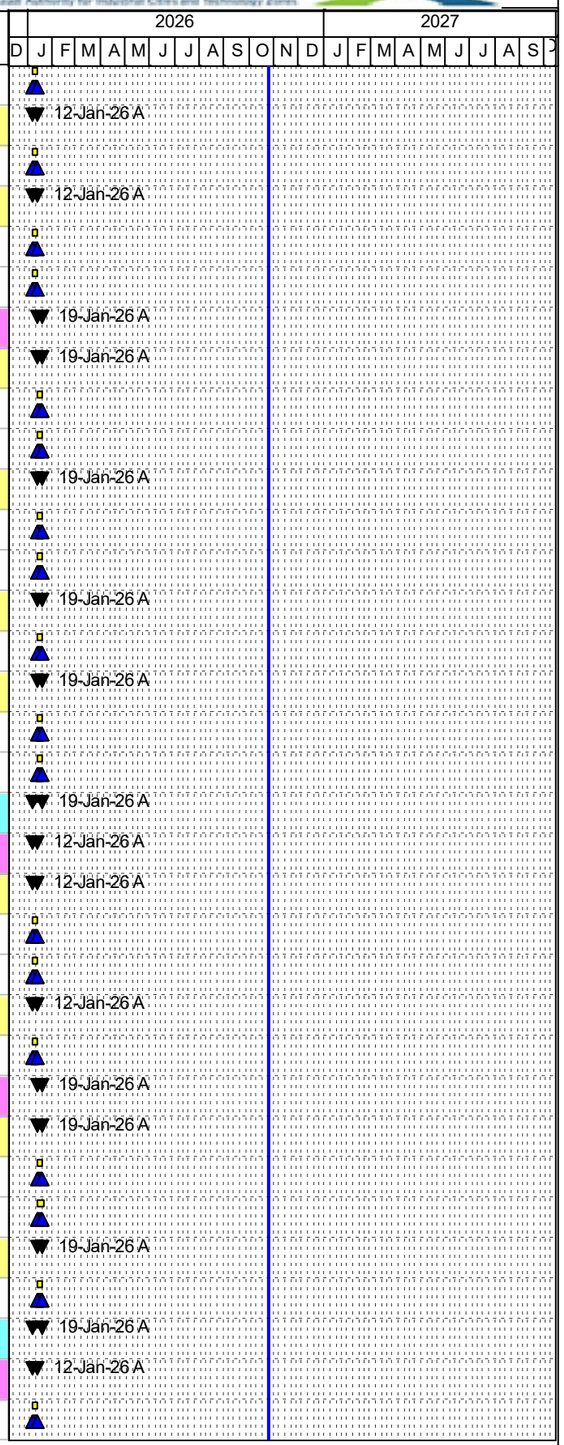

Primary Baseline | Actual Work | Summary
Remaining Work | Baseline Milestone
Critical Remaining Work | Milestone

Date	Revision	Checked	Approved
26-Oct-26	Third Industrial City		


Activity ID	Activity Name	Original Duration	Start	Finish	Budgeted Total Cost	Planned Value Cost	Earned Value Cost	Actual Total Cost	Schedule % Complete	Performance % Complete
Approval of Material		48	13-Jan-26 A	19-Jan-26 A	0	0	0	0	0%	0%
ENG-MT-IR-ML-A-120	Material Approval for Materials of Treated Sewage Effluent (TSE)	48	13-Jan-26 A	19-Jan-26 A	0	0	0	0	100%	100%
Potable Water Network		96	06-Jan-26 A	19-Jan-26 A	0	0	0	0	0%	0%
Submission of Material		56	06-Jan-26 A	12-Jan-26 A	0	0	0	0	0%	0%
Main Line Sections		56	06-Jan-26 A	12-Jan-26 A	0	0	0	0	0%	0%
ENG-MT-PW-ML-S-100	Material Submittal for Main Line Pipes and Materials of Potable Water Network	56	06-Jan-26 A	12-Jan-26 A	0	0	0	0	100%	100%
ENG-MT-PW-ML-S-110	Material Submittal for Main Line Valves of Potable Water Network	56	06-Jan-26 A	12-Jan-26 A	0	0	0	0	100%	100%
Fire Hydrant		56	06-Jan-26 A	12-Jan-26 A	0	0	0	0	0%	0%
ENG-MT-PW-FH-S-100	Material Submittal for Fire Hydrant of Potable Water Network	56	06-Jan-26 A	12-Jan-26 A	0	0	0	0	100%	100%
Testing and Finishes		56	06-Jan-26 A	12-Jan-26 A	0	0	0	0	0%	0%
ENG-MT-PW-TF-S-100	Material Submittal for Surface Box of Potable Water Network	56	06-Jan-26 A	12-Jan-26 A	0	0	0	0	100%	100%
Approval of Material		48	13-Jan-26 A	19-Jan-26 A	0	0	0	0	0%	0%
Main Line Sections		48	13-Jan-26 A	19-Jan-26 A	0	0	0	0	0%	0%
ENG-MT-PW-ML-A-100	Material Approval for Main Line Pipes and Materials of Potable Water Network	48	13-Jan-26 A	19-Jan-26 A	0	0	0	0	100%	100%
ENG-MT-PW-ML-A-110	Material Approval for Valves of Potable Water Network	48	13-Jan-26 A	19-Jan-26 A	0	0	0	0	100%	100%
Fire Hydrant		48	13-Jan-26 A	19-Jan-26 A	0	0	0	0	0%	0%
ENG-MT-PW-FH-A-100	Material Approval for Fire Hydrants of Potable Water Network	48	13-Jan-26 A	19-Jan-26 A	0	0	0	0	100%	100%
Testing and Finishes		48	13-Jan-26 A	19-Jan-26 A	0	0	0	0	0%	0%
ENG-MT-PW-TF-A-100	Material Approval for Surface Box of Potable Water Network	48	13-Jan-26 A	19-Jan-26 A	0	0	0	0	100%	100%
Irrigation Network		96	06-Jan-26 A	19-Jan-26 A	0	0	0	0	0%	0%
Submission of Material		56	06-Jan-26 A	12-Jan-26 A	0	0	0	0	0%	0%
Main Line Pipes		56	06-Jan-26 A	12-Jan-26 A	0	0	0	0	0%	0%
ENG-MT-IR-ML-S-100	Material Submittal for Main Line Pipes of Irrigation Network	56	06-Jan-26 A	12-Jan-26 A	0	0	0	0	100%	100%
ENG-MT-IR-ML-S-110	Material Submittal for Main Line Valves of Irrigation Network	56	06-Jan-26 A	12-Jan-26 A	0	0	0	0	100%	100%
Approval of Material		48	13-Jan-26 A	19-Jan-26 A	0	0	0	0	0%	0%
Main Line Pipes		48	13-Jan-26 A	19-Jan-26 A	0	0	0	0	0%	0%
ENG-MT-IR-ML-A-100	Material Approval for Main Line Pipes of Irrigation Network	48	13-Jan-26 A	19-Jan-26 A	0	0	0	0	100%	100%
ENG-MT-IR-ML-A-110	Material Approval for Valves of Irrigation Network	48	13-Jan-26 A	19-Jan-26 A	0	0	0	0	100%	100%
Medium Voltage Network		96	06-Jan-26 A	19-Jan-26 A	0	0	0	0	0%	0%
Submission of Material		56	06-Jan-26 A	12-Jan-26 A	0	0	0	0	0%	0%
ENG-MT-MV-ML-S-100	Material Submittal for Medium Voltage Materials of Medium Voltage Network	56	06-Jan-26 A	12-Jan-26 A	0	0	0	0	100%	100%
Approval of Material		48	13-Jan-26 A	19-Jan-26 A	0	0	0	0	0%	0%
ENG-MT-MV-ML-A-100	Material Approval for Medium Voltage Materials of Medium Voltage Network	48	13-Jan-26 A	19-Jan-26 A	0	0	0	0	100%	100%
Low Voltage Network		104	06-Jan-26 A	19-Jan-26 A	0	0	0	0	0%	0%

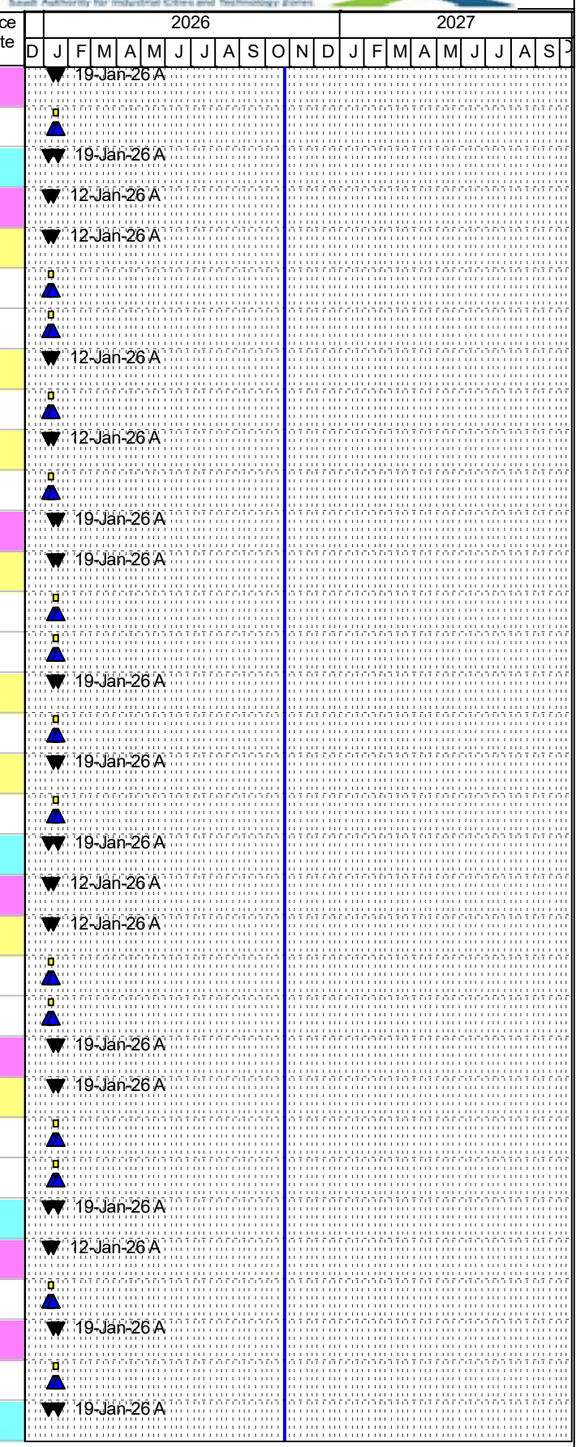

Primary Baseline
Remaining Work
Critical Remaining Work
Actual Work
Baseline Milestone
Milestone
Summary

Date	Revision	Checked	Approved
26-Oct-26	Third Industrial City		


Activity ID	Activity Name	Original Duration	Start	Finish	Budgeted Total Cost	Planned Value Cost	Earned Value Cost	Actual Total Cost	Schedule % Complete	Performance % Complete
Submission of Material		56	06-Jan-26 A	12-Jan-26 A	0	0	0	0	0%	0%
Main Low Voltage Cables Works		56	06-Jan-26 A	12-Jan-26 A	0	0	0	0	0%	0%
PRO-LV-ML-S-100	Material Submittal for Main Low Voltage Cables of Low Voltage Network	56	06-Jan-26 A	12-Jan-26 A	0	0	0	0	100%	100%
Service Low Voltage Cables Works		56	06-Jan-26 A	12-Jan-26 A	0	0	0	0	0%	0%
PRO-LV-HC-S-100	Material Submittal for Service Low Voltage Cables of Low Voltage Network	56	06-Jan-26 A	12-Jan-26 A	0	0	0	0	100%	100%
Distribution Pillars Works		56	06-Jan-26 A	12-Jan-26 A	0	0	0	0	0%	0%
PRO-LV-DP-S-100	Material Submittal for Distribution Pillars of Low Voltage Network	56	06-Jan-26 A	12-Jan-26 A	0	0	0	0	100%	100%
PRO-LV-DP-S-110	Material Submittal for Low Voltage Earthing of Low Voltage Network	56	06-Jan-26 A	12-Jan-26 A	0	0	0	0	100%	100%
Termination and Testing Works		56	06-Jan-26 A	12-Jan-26 A	0	0	0	0	0%	0%
PRO-LV-TT-S-100	Material Submittal for Cable Lugs of Low Voltage Network	56	06-Jan-26 A	12-Jan-26 A	0	0	0	0	100%	100%
Approval of Material		56	13-Jan-26 A	19-Jan-26 A	0	0	0	0	0%	0%
Main Low Voltage Cables Works		48	13-Jan-26 A	19-Jan-26 A	0	0	0	0	0%	0%
PRO-LV-ML-A-100	Material Approval for Main Low Voltage Cables of Low Voltage Network	48	13-Jan-26 A	19-Jan-26 A	0	0	0	0	100%	100%
Service Low Voltage Cables Works		48	13-Jan-26 A	19-Jan-26 A	0	0	0	0	0%	0%
PRO-LV-HC-A-100	Material Approval for Service Low Voltage Cables of Low Voltage Network	48	13-Jan-26 A	19-Jan-26 A	0	0	0	0	100%	100%
Distribution Pillars Works		48	13-Jan-26 A	19-Jan-26 A	0	0	0	0	0%	0%
PRO-LV-DP-A-100	Material Approval for Distribution Pillars of Low Voltage Network	48	13-Jan-26 A	19-Jan-26 A	0	0	0	0	100%	100%
PRO-LV-DP-A-110	Material Approval for Low Voltage Earthing of Low Voltage Network	48	13-Jan-26 A	19-Jan-26 A	0	0	0	0	100%	100%
Termination and Testing Works		56	13-Jan-26 A	19-Jan-26 A	0	0	0	0	0%	0%
PRO-LV-TT-A-100	Material Approval for Cable Lugs of Low Voltage Network	56	13-Jan-26 A	19-Jan-26 A	0	0	0	0	100%	100%
Street Lighting Network		96	06-Jan-26 A	19-Jan-26 A	0	0	0	0	0%	0%
Submission of Material		56	06-Jan-26 A	12-Jan-26 A	0	0	0	0	0%	0%
Cabling Works		56	06-Jan-26 A	12-Jan-26 A	0	0	0	0	0%	0%
ENG-MT-SL-ML-S-100	Material Submittal for Lighting Cables of Street Lighting Network	56	06-Jan-26 A	12-Jan-26 A	0	0	0	0	100%	100%
Lighting Poles Works		56	06-Jan-26 A	12-Jan-26 A	0	0	0	0	0%	0%
ENG-MT-SL-S-100	Material Submittal for Lighting Poles Concrete Foundations of Street Lighting Network	56	06-Jan-26 A	12-Jan-26 A	0	0	0	0	100%	100%
ENG-MT-SL-S-110	Material Submittal for Lighting Poles of Street Lighting Network	56	06-Jan-26 A	12-Jan-26 A	0	0	0	0	100%	100%
ENG-MT-SL-S-120	Material Submittal for Lighting Fixtures of Street Lighting Network	56	06-Jan-26 A	12-Jan-26 A	0	0	0	0	100%	100%
Distribution Panel Board		56	06-Jan-26 A	12-Jan-26 A	0	0	0	0	0%	0%
ENG-MT-SL-DB-S-100	Material Submittal for Lighting Distrubution Panel Boards of Street Lighting Network	56	06-Jan-26 A	12-Jan-26 A	0	0	0	0	100%	100%
Termination and Testing Works		56	06-Jan-26 A	12-Jan-26 A	0	0	0	0	0%	0%
ENG-MT-SL-TF-S-100	Material Submittal for Fuse Boxes of Street Lighting Network	56	06-Jan-26 A	12-Jan-26 A	0	0	0	0	100%	100%
ENG-MT-SL-TF-S-110	Material Submittal for Cable Lugs of Street Lighting Network	56	06-Jan-26 A	12-Jan-26 A	0	0	0	0	100%	100%
Earthing System Works		56	06-Jan-26 A	12-Jan-26 A	0	0	0	0	0%	0%

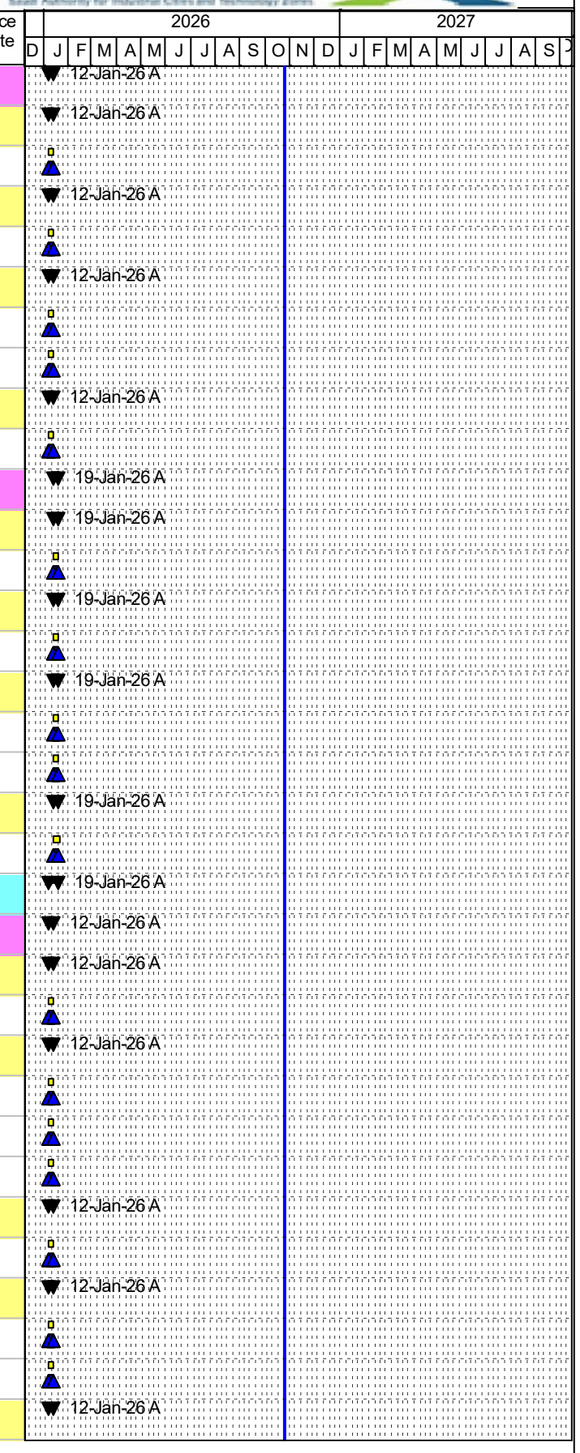

Primary Baseline | Actual Work | Summary
Remaining Work | Baseline Milestone
Critical Remaining Work | Milestone

Date	Revision	Checked	Approved
26-Oct-26	Third Industrial City		


Activity ID	Activity Name	Original Duration	Start	Finish	Budgeted Total Cost	Planned Value Cost	Earned Value Cost	Actual Total Cost	Schedule % Complete	Performance % Complete
ENG-MT-SL-ES-S-100	Material Submittal for Lighting Earthing of Street Lighting Network	56	06-Jan-26 A	12-Jan-26 A	0	0	0	0	100%	100%
Approval of Material		48	13-Jan-26 A	19-Jan-26 A	0	0	0	0	0%	0%
Cabling Works		48	13-Jan-26 A	19-Jan-26 A	0	0	0	0	0%	0%
ENG-MT-SL-ML-A-100	Material Approval for Lighting Cables of Street Lighting Network	48	13-Jan-26 A	19-Jan-26 A	0	0	0	0	100%	100%
Lighting Poles Works		48	13-Jan-26 A	19-Jan-26 A	0	0	0	0	0%	0%
ENG-MT-SL-A-100	Material Approval for Lighting Poles Concrete Foundations of Street Lighting Network	48	13-Jan-26 A	19-Jan-26 A	0	0	0	0	100%	100%
ENG-MT-SL-A-110	Material Approval for Lighting Poles of Street Lighting Network	48	13-Jan-26 A	19-Jan-26 A	0	0	0	0	100%	100%
ENG-MT-SL-A-120	Material Approval for Lighting Fixtures of Street Lighting Network	48	13-Jan-26 A	19-Jan-26 A	0	0	0	0	100%	100%
Distribution Panel Board		48	13-Jan-26 A	19-Jan-26 A	0	0	0	0	0%	0%
ENG-MT-SL-DB-A-100	Material Approval for Distrubution Panel Boards of Street Lighting Network	48	13-Jan-26 A	19-Jan-26 A	0	0	0	0	100%	100%
Termination and Testing Works		48	13-Jan-26 A	19-Jan-26 A	0	0	0	0	0%	0%
ENG-MT-SL-TF-A-100	Material Approval for Fuse Boxes of Street Lighting Network	48	13-Jan-26 A	19-Jan-26 A	0	0	0	0	100%	100%
ENG-MT-SL-TF-A-110	Material Approval for Cable Lugs of Street Lighting Network	48	13-Jan-26 A	19-Jan-26 A	0	0	0	0	100%	100%
Earthing System Works		48	13-Jan-26 A	19-Jan-26 A	0	0	0	0	0%	0%
ENG-MT-SL-ES-A-100	Material Approval for Lighting Earthing of Street Lighting Network	48	13-Jan-26 A	19-Jan-26 A	0	0	0	0	100%	100%
Telecom and Light Current Networks		96	06-Jan-26 A	19-Jan-26 A	0	0	0	0	0%	0%
Submission of Material		56	06-Jan-26 A	12-Jan-26 A	0	0	0	0	0%	0%
Ducts Works		56	06-Jan-26 A	12-Jan-26 A	0	0	0	0	0%	0%
ENG-MT-TE-S-100	Material Submittal for Ducts of Telecom Network	56	06-Jan-26 A	12-Jan-26 A	0	0	0	0	100%	100%
Manholes Works		56	06-Jan-26 A	12-Jan-26 A	0	0	0	0	0%	0%
ENG-MT-TE-S-110	Material Submittal for Manholes of Telecom Network	56	06-Jan-26 A	12-Jan-26 A	0	0	0	0	100%	100%
CCTV, Telephone, MSN, ACs System Works		56	06-Jan-26 A	12-Jan-26 A	0	0	0	0	0%	0%
ENG-MT-CTV-S-100	Material Submittal for Materials of CCTV, Telephone, MSN, and Access Control	56	06-Jan-26 A	12-Jan-26 A	0	0	0	0	100%	100%
Approval of Material		48	13-Jan-26 A	19-Jan-26 A	0	0	0	0	0%	0%
Ducts Works		48	13-Jan-26 A	19-Jan-26 A	0	0	0	0	0%	0%
ENG-MT-TE-A-100	Material Approval for Ducts of Telecom Network	48	13-Jan-26 A	19-Jan-26 A	0	0	0	0	100%	100%
Manholes Works		48	13-Jan-26 A	19-Jan-26 A	0	0	0	0	0%	0%
ENG-MT-TE-A-110	Material Approval for Manholes of Telecom Network	48	13-Jan-26 A	19-Jan-26 A	0	0	0	0	100%	100%
CCTV, Telephone, MSN, ACs System Works		48	13-Jan-26 A	19-Jan-26 A	0	0	0	0	0%	0%
ENG-MT-CTV-A-100	Material Approval for for Materials of CCTV, Telephone, MSN, and Access Control	48	13-Jan-26 A	19-Jan-26 A	0	0	0	0	100%	100%
Road Works		184	06-Jan-26 A	31-Jan-26 A	0	0	0	0	0%	0%
Submission of Material		136	06-Jan-26 A	24-Jan-26 A	0	0	0	0	0%	0%
General Road Works		56	18-Jan-26 A	24-Jan-26 A	0	0	0	0	0%	0%
ENG-MT-RD-S-100	Material Submittal for Subgrade of Road Works	56	18-Jan-26 A	24-Jan-26 A	0	0	0	0	100%	100%

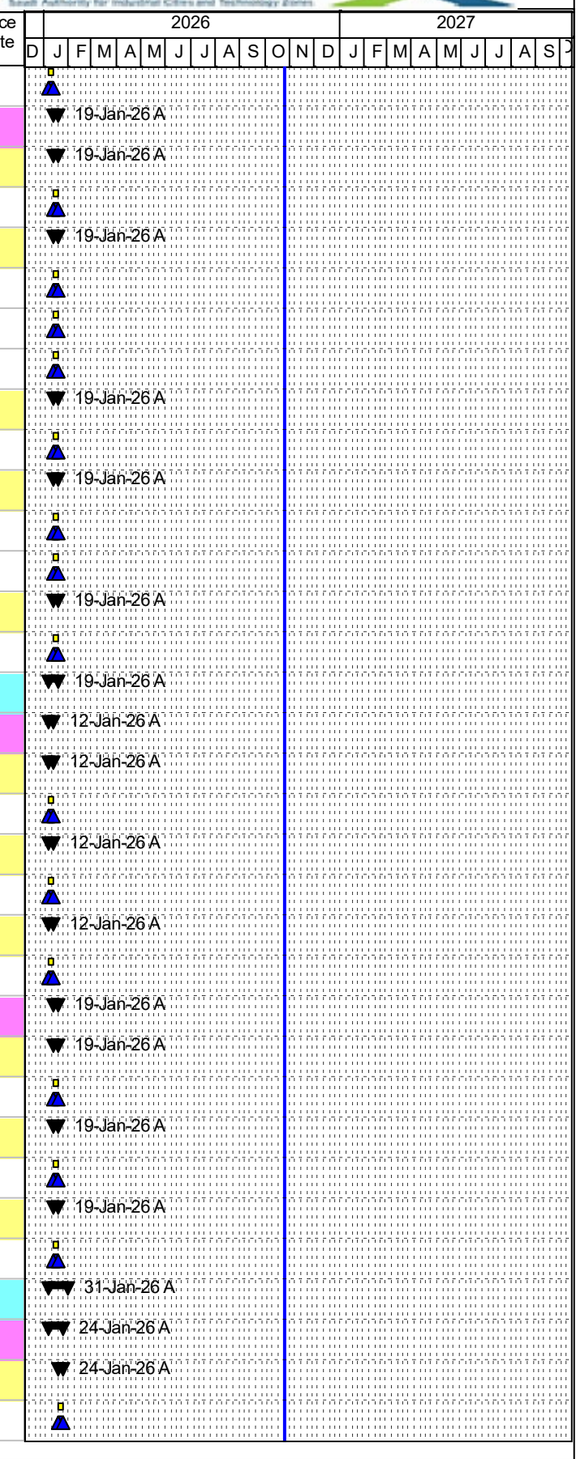

Primary Baseline
Remaining Work
Critical Remaining Work
Actual Work
Baseline Milestone
Milestone
Summary

Date	Revision	Checked	Approved
26-Oct-26	Third Industrial City		

Activity ID	Activity Name	Original Duration	Start	Finish	Budgeted Total Cost	Planned Value Cost	Earned Value Cost	Actual Total Cost	Schedule % Complete	Performance % Complete
ENG-MT-RD-S-110	Material Submittal for Aggregate Base Course of Road Works	56	18-Jan-26 A	24-Jan-26 A	0	0	0	0	100%	100%
ENG-MT-RD-S-120	Material Submittal for Prime Coat of Road Works	56	18-Jan-26 A	24-Jan-26 A	0	0	0	0	100%	100%
ENG-MT-RD-S-130	Material Submittal for Asphaltic Base Course Laver of Road Works	56	18-Jan-26 A	24-Jan-26 A	0	0	0	0	100%	100%
ENG-MT-RD-S-160	Material Submittal for Asphaltic Wearing Course Laver for Roads Network	56	18-Jan-26 A	24-Jan-26 A	0	0	0	0	100%	100%
ENG-MT-RD-S-170	Material Submittal for Tack Coat Layer for Roads Network	56	18-Jan-26 A	24-Jan-26 A	0	0	0	0	100%	100%
Landscape Works		56	06-Jan-26 A	12-Jan-26 A	0	0	0	0	0%	0%
ENG-MT-RD-S-140	Material Submittal for Interlock Tiles of Landscaping	56	06-Jan-26 A	12-Jan-26 A	0	0	0	0	100%	100%
ENG-MT-RD-S-150	Material Submittal for Curbstones of Landscaping	56	06-Jan-26 A	12-Jan-26 A	0	0	0	0	100%	100%
Traffic Signs Boards and Roads Marking		56	06-Jan-26 A	12-Jan-26 A	0	0	0	0	0%	0%
ENG-MT-TS-S-100	Material Submittal for Traffic Signs Boards of Road Works	56	06-Jan-26 A	12-Jan-26 A	0	0	0	0	100%	100%
ENG-MT-TS-S-110	Material Submittal for Road Markings of Road Works	56	06-Jan-26 A	12-Jan-26 A	0	0	0	0	100%	100%
Approval of Material		136	13-Jan-26 A	31-Jan-26 A	0	0	0	0	0%	0%
General Road Works		56	25-Jan-26 A	31-Jan-26 A	0	0	0	0	0%	0%
ENG-MT-RD-A-100	Material Approval for Subgrade of Road Works	48	25-Jan-26 A	31-Jan-26 A	0	0	0	0	100%	100%
ENG-MT-RD-A-110	Material Approval for Aggregate Base Course of Road Works	48	25-Jan-26 A	31-Jan-26 A	0	0	0	0	100%	100%
ENG-MT-RD-A-120	Material Approval for Prime Coat of Road Works	48	25-Jan-26 A	31-Jan-26 A	0	0	0	0	100%	100%
ENG-MT-RD-A-130	Material Approval for Asphaltic Base Course Layer of Road Works	56	25-Jan-26 A	31-Jan-26 A	0	0	0	0	100%	100%
ENG-MT-RD-A-160	Material Approval for Asphaltic Wearing Course Laver for Roads Network	56	25-Jan-26 A	31-Jan-26 A	0	0	0	0	100%	100%
ENG-MT-RD-A-170	Material Approval for Tack Coat Layer for Roads Network	48	25-Jan-26 A	31-Jan-26 A	0	0	0	0	100%	100%
Landscape Works		48	13-Jan-26 A	19-Jan-26 A	0	0	0	0	0%	0%
ENG-MT-RD-A-140	Material Approval of Interlock Tiles for Landscaping	48	13-Jan-26 A	19-Jan-26 A	0	0	0	0	100%	100%
ENG-MT-RD-A-150	Material Approval of Curbstones for Landscaping	48	13-Jan-26 A	19-Jan-26 A	0	0	0	0	100%	100%
Traffic Signs Boards and Roads Marking		48	13-Jan-26 A	19-Jan-26 A	0	0	0	0	0%	0%
ENG-MT-TS-A-100	Material Approval for Traffic Signs Boards of Road Works	48	13-Jan-26 A	19-Jan-26 A	0	0	0	0	100%	100%
ENG-MT-TS-A-110	Material Approval for Road Markings of Road Works	48	13-Jan-26 A	19-Jan-26 A	0	0	0	0	100%	100%
Softscape and Planting Works		96	06-Jan-26 A	19-Jan-26 A	0	0	0	0	0%	0%
Submission of Material		56	06-Jan-26 A	12-Jan-26 A	0	0	0	0	0%	0%
ENG-MT-IR-ML-S-140	Material Submittal for Softscape and Planting Works	56	06-Jan-26 A	12-Jan-26 A	0	0	0	0	100%	100%
ENG-MT-IR-ML-S-150	Material Submittal for Site Furnishings (Seating Bench,Stone Boulders and Gravel)	56	06-Jan-26 A	12-Jan-26 A	0	0	0	0	100%	100%
Approval of Material		48	13-Jan-26 A	19-Jan-26 A	0	0	0	0	0%	0%
ENG-MT-IR-ML-A-140	Material Approval for Softscape and Planting Works	48	13-Jan-26 A	19-Jan-26 A	0	0	0	0	100%	100%
ENG-MT-IR-ML-A-150	Material Approval for Site Furnishings (Seating Bench,Stone Boulders and Gravel)	48	13-Jan-26 A	19-Jan-26 A	0	0	0	0	100%	100%
Superstructure Works		992	06-Jan-26 A	13-Jun-26 A	0	0	0	0	0%	0%
Water Pump Station		96	06-Jan-26 A	19-Jan-26 A	0	0	0	0	0%	0%

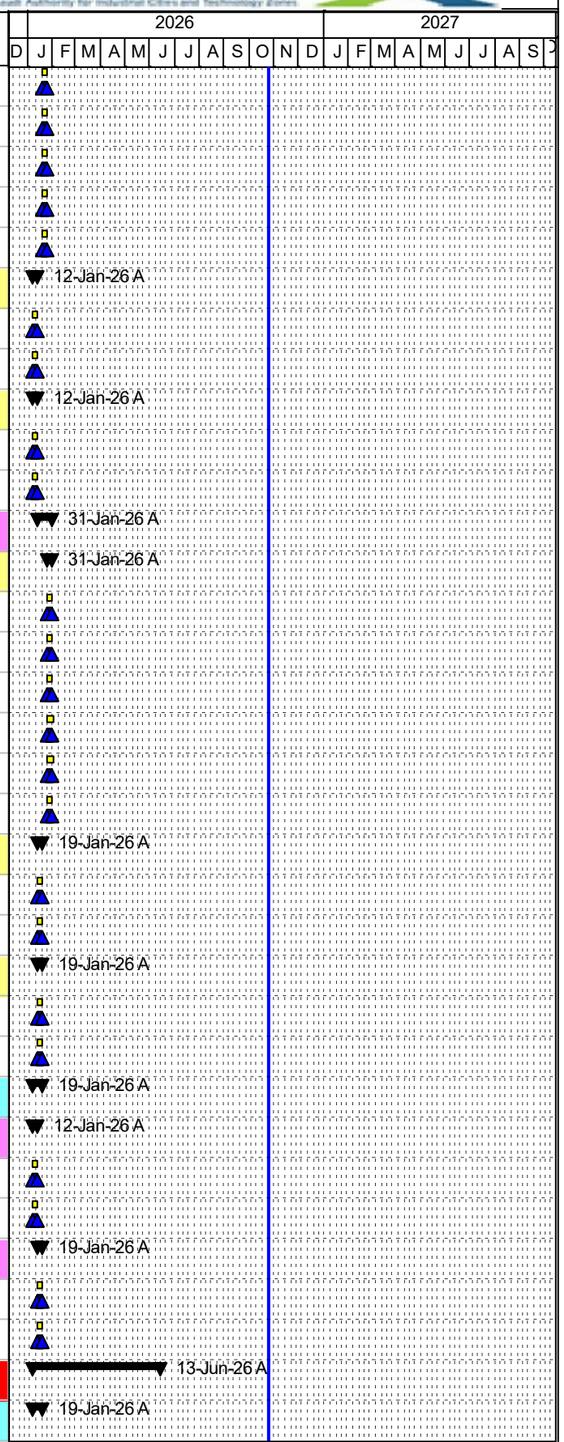


Primary Baseline
Remaining Work
Critical Remaining Work
Actual Work
Baseline Milestone
Milestone
Summary

Date	Revision	Checked	Approved
26-Oct-26	Third Industrial City		

Development of the Technology City in Dharan Project
BL-Update 26-10-2026
WPR UPS LEVEL 5

Activity ID	Activity Name	Original Duration	Start	Finish	Budgeted Total Cost	Planned Value Cost	Earned Value Cost	Actual Total Cost	Schedule % Complete	Performance % Complete
Submission of Material		56	06-Jan-26 A	12-Jan-26 A	0	0	0	0	0%	0%
ENG-MT-SLS-CV-S-100	Material Submittal for Works for Water Pump Station	56	06-Jan-26 A	12-Jan-26 A	0	0	0	0	100%	100%
Approval of Material		48	13-Jan-26 A	19-Jan-26 A	0	0	0	0	0%	0%
ENG-MT-SLS-CV-A-110	Material Approval for Works for Water Pump Station	48	13-Jan-26 A	19-Jan-26 A	0	0	0	0	100%	100%
Storage Tank (TSE)		96	06-Jan-26 A	19-Jan-26 A	0	0	0	0	0%	0%
Submission of Material		56	06-Jan-26 A	12-Jan-26 A	0	0	0	0	0%	0%
ENG-MT-TSE-CV-S-130	Material Submittal for Works for Storage Tank (TSE)	56	06-Jan-26 A	12-Jan-26 A	0	0	0	0	100%	100%
Approval of Material		48	13-Jan-26 A	19-Jan-26 A	0	0	0	0	0%	0%
ENG-MT-TSE-CV-A-140	Material Approval for Works for Storage Tank (TSE)	48	13-Jan-26 A	19-Jan-26 A	0	0	0	0	100%	100%
Control Room		56	03-Feb-26 A	10-Feb-26 A	0	0	0	0	0%	0%
Submission of Material		24	03-Feb-26 A	04-Feb-26 A	0	0	0	0	0%	0%
ENG-MT-TSE-CV-S-140	Material Submittal for Works for Control Room	24	03-Feb-26 A	04-Feb-26 A	0	0	0	0	100%	100%
Approval of Material		48	04-Feb-26 A	10-Feb-26 A	0	0	0	0	0%	0%
ENG-MT-TSE-CV-A-150	Material Approval for Works for Control Room	48	04-Feb-26 A	10-Feb-26 A	0	0	0	0	100%	100%
Sewage Pump Stations		288	06-Jan-26 A	16-Feb-26 A	0	0	0	0	0%	0%
Submission of Material		56	06-Jan-26 A	12-Jan-26 A	0	0	0	0	0%	0%
ENG-MT-PS-CV-S-140	Material Submittal for Works of Sewage Pump Station	56	06-Jan-26 A	12-Jan-26 A	0	0	0	0	100%	100%
Approval of Material		40	11-Feb-26 A	16-Feb-26 A	0	0	0	0	0%	0%
ENG-MT-PS-CV-A-150	Material Approval for Works of Sewage Pump Station	40	11-Feb-26 A	16-Feb-26 A	0	0	0	0	100%	100%
Gaurd Room		64	18-Feb-26 A	02-Mar-26 A	0	0	0	0	0%	0%
Submission of Material		0	18-Feb-26 A	19-Feb-26 A	0	0	0	0	0%	0%
ENG-MT-GR-CV-S-120	Material Submittal for Materials for Gaurd Room	0	18-Feb-26 A	19-Feb-26 A	0	0	0	0	100%	100%
Approval of Material		56	19-Feb-26 A	02-Mar-26 A	0	0	0	0	0%	0%
ENG-MT-GR-CV-A-130	Material Approval for Materials for Gaurd Room	56	19-Feb-26 A	02-Mar-26 A	0	0	0	0	100%	100%
Boundary Fence		656	25-Feb-26 A	13-Jun-26 A	0	0	0	0	0%	0%
Submission of Material		0	25-Feb-26 A	26-Feb-26 A	0	0	0	0	0%	0%
ENG-MT-FE-CV-S-110	Material Submittal for Materials for Boundary Fence	0	25-Feb-26 A	26-Feb-26 A	0	0	0	0	100%	100%
Approval of Material		640	28-Feb-26 A	13-Jun-26 A	0	0	0	0	0%	0%
ENG-MT-FE-CV-A-120	Material Approval for Materials for Boundary Fence	640	28-Feb-26 A	13-Jun-26 A	0	0	0	0	100%	100%
Long Lead Time Items		192	26-Oct-26	22-Nov-26	0	0	0	0	0%	0%
Superstructure Works		192	26-Oct-26	22-Nov-26	0	0	0	0	0%	0%
Sewage Pump Stations		96	26-Oct-26	08-Nov-26	0	0	0	0	0%	0%
Submission of Material		48	26-Oct-26	01-Nov-26	0	0	0	0	0%	0%
ENG-MT-SPS-MC-S-100	Material Submittal for Electromechanical Works for Pump Station	48	26-Oct-26	01-Nov-26	0	0	0	0	100%	0%

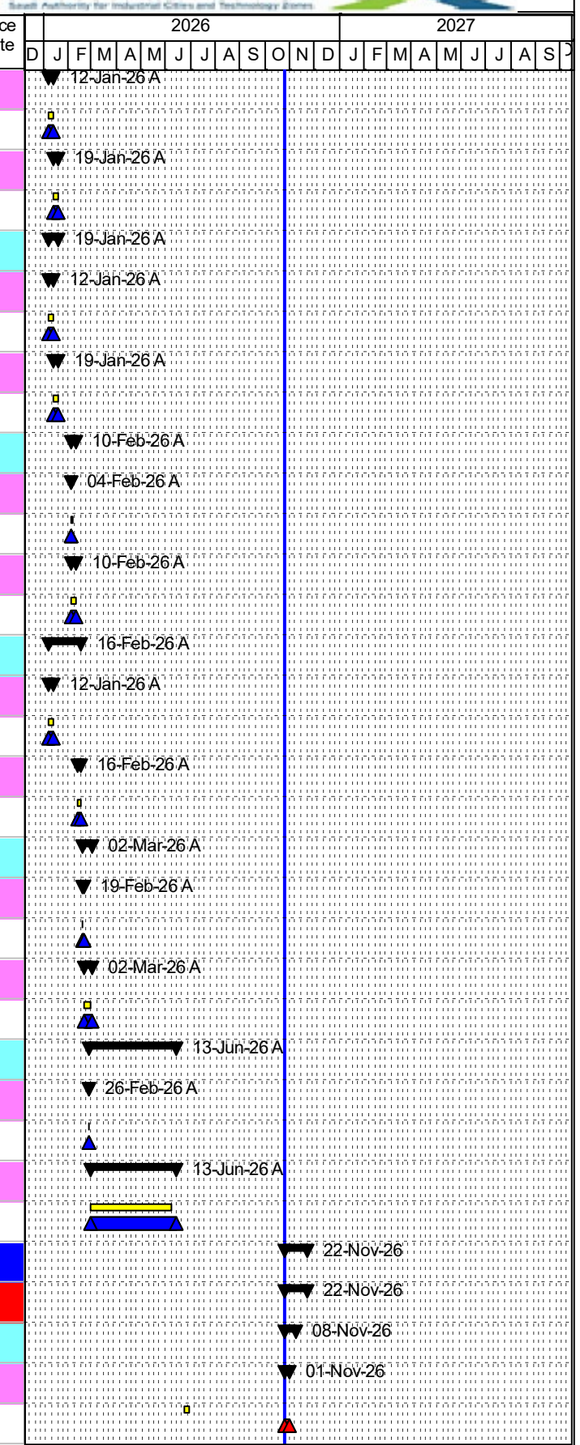


Primary Baseline
Remaining Work
Critical Remaining Work
Actual Work
Baseline Milestone
Milestone
Summary

Date	Revision	Checked	Approved
26-Oct-26	Third Industrial City		

Development of the Technology City in Dharan Project
BL-Update 26-10-2026
WPR UPS LEVEL 5

Activity ID	Activity Name	Original Duration	Start	Finish	Budgeted Total Cost	Planned Value Cost	Earned Value Cost	Actual Total Cost	Schedule % Complete	Performance % Complete
Approval of Material		48	02-Nov-26	08-Nov-26	0	0	0	0	0%	0%
ENG-MT-SPS-MC-A-110	Material Approval for Electromechanical Works for Pump Station	48	02-Nov-26	08-Nov-26	0	0	0	0	100%	0%
Storage Tank (TSE)		192	26-Oct-26	22-Nov-26	0	0	0	0	0%	0%
Submission of Material		96	26-Oct-26	08-Nov-26	0	0	0	0	0%	0%
ENG-MT-TSE-MC-S-110	Material Submittal for Electromechanical Works for Storage Tank (TSE)	96	26-Oct-26	08-Nov-26	0	0	0	0	100%	0%
Approval of Material		96	09-Nov-26	22-Nov-26	0	0	0	0	0%	0%
ENG-MT-TSE-MC-A-120	Material Approval for Electromechanical Works for Storage Tank (TSE)	96	09-Nov-26	22-Nov-26	0	0	0	0	100%	0%
Procurement Cycle		2744	02-May-26 A	20-Jun-27	0	0	0	0	0%	0%
Short Lead Time Items		2448	02-May-26 A	02-May-27	0	0	0	0	0%	0%
Infrastructure Networks		2448	02-May-26 A	02-May-27	0	0	0	0	0%	0%
Storm Drainage Network		1080	01-Jul-26 A	06-Mar-27	0	0	0	0	0%	0%
Issuance of Purchase Orders		424	01-Jul-26 A	30-Nov-26	0	0	0	0	0%	0%
Main Line Sections		192	01-Jul-26 A	27-Oct-26	0	0	0	0	0%	0%
PRO-SD-PO-100	Issuance of Purchase Order for Manholes of Storm Drainage Network	16	26-Oct-26	27-Oct-26	0	0	0	0	100%	0%
PRO-SD-PO-110	Issuance of Purchase Order for Main Line Pipes of Storm Drainage Network	16	01-Jul-26 A	02-Jul-26 A	0	0	0	0	100%	100%
Catch Basin Sections		88	28-Oct-26	09-Nov-26	0	0	0	0	0%	0%
PRO-SD-PO-130	Issuance of Purchase Order for Catch Basins of Storm Drainage Network	40	28-Oct-26	02-Nov-26	0	0	0	0	100%	0%
PRO-SD-PO-150	Issuance of Purchase Order for Catch Basin Pipes of Storm Drainage Network	48	03-Nov-26	09-Nov-26	0	0	0	0	100%	0%
Testing and Finishes		96	10-Nov-26	23-Nov-26	0	0	0	0	0%	0%
PRO-SD-PO-120	Issuance of Purchase Order for Manhole Covers of Storm Drainage Network	48	10-Nov-26	16-Nov-26	0	0	0	0	100%	0%
PRO-SD-PO-140	Issuance of Purchase Order for Catch Basin Covers of Storm Drainage Network	48	17-Nov-26	23-Nov-26	0	0	0	0	100%	0%
Storm Drainage Ponds		48	24-Nov-26	30-Nov-26	0	0	0	0	0%	0%
PRO-DPO-CV-PO-10	Issuance of Purchase Order for Materials of Storm Drainage Ponds	48	24-Nov-26	30-Nov-26	0	0	0	0	100%	0%
Manufacturing of Material		920	05-Jul-26 A	13-Feb-27	0	0	0	0	0%	0%
Main Line Sections		240	05-Jul-26 A	05-Nov-26	0	0	0	0	0%	0%
PRO-SD-MF-100	Manufacturing of Materials for Manholes of Storm Drainage Network	64	28-Oct-26	05-Nov-26	0	0	0	0	100%	0%
PRO-SD-MF-110	Manufacturing of Materials for Main Line Pipes of Storm Drainage Network	192	05-Jul-26 A	07-Jul-26 A	0	0	0	0	100%	100%
Catch Basin Sections		248	03-Nov-26	08-Dec-26	0	0	0	0	0%	0%
PRO-SD-MF-130	Manufacturing of Materials for Catch Basins of Storm Drainage Network	200	03-Nov-26	01-Dec-26	0	0	0	0	100%	0%
PRO-SD-MF-150	Manufacturing of Materials for Catch Basin Pipes of Storm Drainage Network	200	10-Nov-26	08-Dec-26	0	0	0	0	100%	0%
Testing and Finishes		400	09-Dec-26	04-Feb-27	0	0	0	0	0%	0%
PRO-SD-MF-120	Manufacturing of Materials for Manhole Covers of Storm Drainage Network	160	09-Dec-26	31-Dec-26	0	0	0	0	100%	0%
PRO-SD-MF-140	Manufacturing of Materials for Catch Basin Covers of Storm Drainage Network	240	02-Jan-27	04-Feb-27	0	0	0	0	100%	0%
Storm Drainage Ponds		512	01-Dec-26	13-Feb-27	0	0	0	0	0%	0%

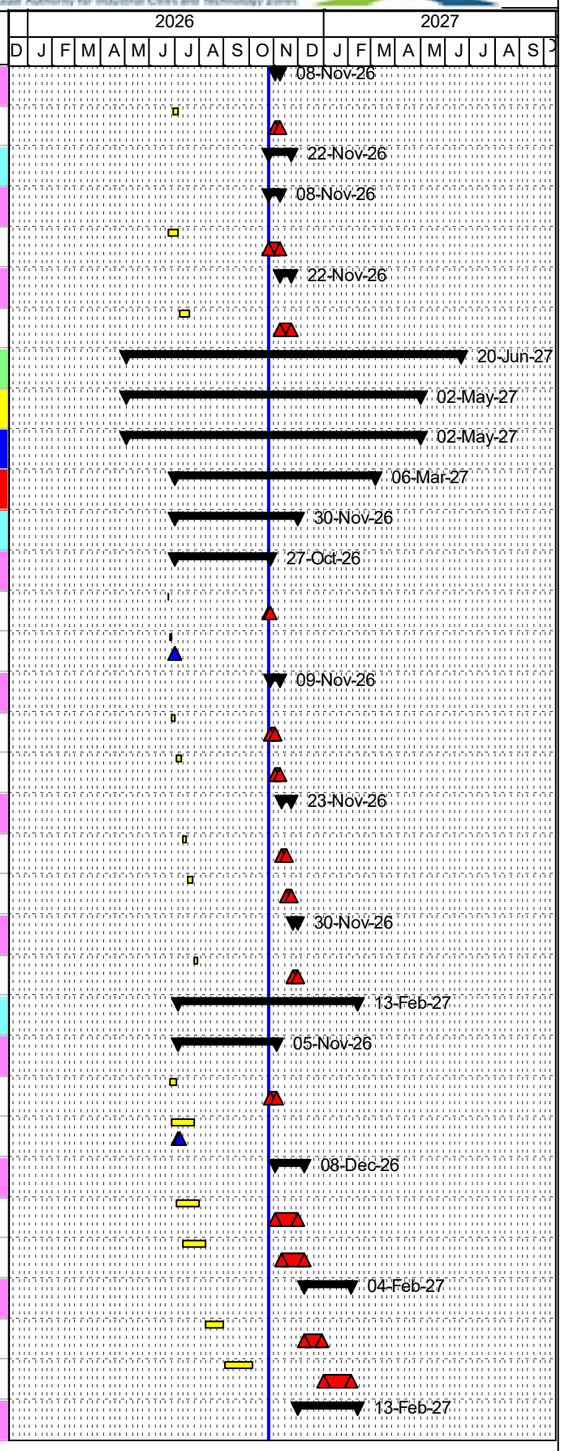


Primary Baseline | Actual Work | Summary
Remaining Work | Baseline Milestone
Critical Remaining Work | Milestone

Date	Revision	Checked	Approved
26-Oct-26	Third Industrial City		

Development of the Technology City in Dharan Project
BL-Update 26-10-2026
WPR UPS LEVEL 5

Activity ID	Activity Name	Original Duration	Start	Finish	Budgeted Total Cost	Planned Value Cost	Earned Value Cost	Actual Total Cost	Schedule % Complete	Performance % Complete
PRO-DPO-CV-MF-10	Manufacturing of Materials of Storm Drainage Ponds	512	01-Dec-26	13-Feb-27	0	0	0	0	100%	0%
1st Material Delivery & Site Inspection		760	08-Jul-26 A	17-Feb-27	0	0	0	0	0%	0%
Main Line Sections		80	08-Jul-26 A	10-Nov-26	0	0	0	0	0%	0%
PRO-SD-1DL-100	1ST Material Delivery for Manholes of Storm Drainage Network	32	07-Nov-26	10-Nov-26	0	0	0	0	100%	0%
PRO-SD-1DL-110	1ST Material Delivery for Main Line Pipes of Storm Drainage Network	32	08-Jul-26 A	12-Jul-26 A	0	0	0	0	100%	100%
Catch Basin Sections		80	02-Dec-26	13-Dec-26	0	0	0	0	0%	0%
PRO-SD-1DL-120	1ST Material Delivery for Catch Basin Pipes of Storm Drainage Network	32	09-Dec-26	13-Dec-26	0	0	0	0	100%	0%
PRO-SD-1DL-130	1ST Material Delivery for Catch Basins of Storm Drainage Network	32	02-Dec-26	06-Dec-26	0	0	0	0	100%	0%
Testing and Finishes		272	02-Jan-27	09-Feb-27	0	0	0	0	0%	0%
PRO-SD-1DL-140	1ST Material Delivery for Manholes Covers of Storm Drainage Network	32	02-Jan-27	05-Jan-27	0	0	0	0	100%	0%
PRO-SD-1DL-150	1ST Material Delivery for Catch Basin Covers of Storm Drainage Network	32	06-Feb-27	09-Feb-27	0	0	0	0	100%	0%
Storm Drainage Ponds		32	14-Feb-27	17-Feb-27	0	0	0	0	0%	0%
PRO-DPO-CV-1DL-10	1ST Material Delivery for Materials of Drainage Ponds	32	14-Feb-27	17-Feb-27	0	0	0	0	100%	0%
Material Delivery & Site Inspection		840	20-Jul-26 A	06-Mar-27	0	0	0	0	0%	0%
Main Line Sections		128	20-Jul-26 A	09-Dec-26	0	0	0	0	0%	0%
PRO-R25-SD-DL-100	Material Delivery & Site Inspection of Manholes of Storm Drainage Network	80	11-Nov-26	22-Nov-26	0	0	0	0	100%	0%
PRO-R25-SD-DL-120	Material Delivery & Site Inspection of Main Line Pipes of Storm Drainage Network	120	20-Jul-26 A	09-Dec-26	0	0	0	0	100%	95%
Catch Basin Sections		120	07-Dec-26	23-Dec-26	0	0	0	0	0%	0%
PRO-R25-SD-DL-110	Material Delivery & Site Inspection of Catch Basin Pipes for Storm Drainage Network	56	16-Dec-26	23-Dec-26	0	0	0	0	100%	0%
PRO-R25-SD-DL-130	Material Delivery & Site Inspection of Catch Basins for Storm Drainage Network	64	07-Dec-26	15-Dec-26	0	0	0	0	100%	0%
Testing and Finishes		352	06-Jan-27	25-Feb-27	0	0	0	0	0%	0%
PRO-R25-SD-DL-140	Material Delivery & Site Inspection of Manholes Covers for Storm Drainage Network	160	06-Jan-27	28-Jan-27	0	0	0	0	100%	0%
PRO-R25-SD-DL-150	Material Delivery & Site Inspection of Catch Basin Covers for Storm Drainage Network	112	10-Feb-27	25-Feb-27	0	0	0	0	85.71%	0%
Storm Drainage Ponds		112	18-Feb-27	06-Mar-27	0	0	0	0	0%	0%
PRO-DPO-CV-DL-10	Material Delivery & Site Inspection for Materials of Storm Drainage Ponds	112	18-Feb-27	06-Mar-27	0	0	0	0	35.71%	0%
Sewage Network		328	26-Oct-26	12-Dec-26	0	0	0	0	0%	0%
Issuance of Purchase Orders		168	26-Oct-26	18-Nov-26	0	0	0	0	0%	0%
Main Line Sections		112	26-Oct-26	10-Nov-26	0	0	0	0	0%	0%
PRO-SW-PO-100	Issuance of Purchase Order for Main Line Pipes of Sewage Network	56	26-Oct-26	02-Nov-26	0	0	0	0	100%	0%
PRO-SW-PO-110	Issuance of Purchase Order for Manhole of Sewage Network	56	03-Nov-26	10-Nov-26	0	0	0	0	100%	0%
Testing and Finishes		56	11-Nov-26	18-Nov-26	0	0	0	0	0%	0%
PRO-SW-PO-120	Issuance of Purchase Order for Manhole Covers of Sewage Network	56	11-Nov-26	18-Nov-26	0	0	0	0	100%	0%
Manufacturing of Material		160	03-Nov-26	25-Nov-26	0	0	0	0	0%	0%
Main Line Sections		136	03-Nov-26	22-Nov-26	0	0	0	0	0%	0%

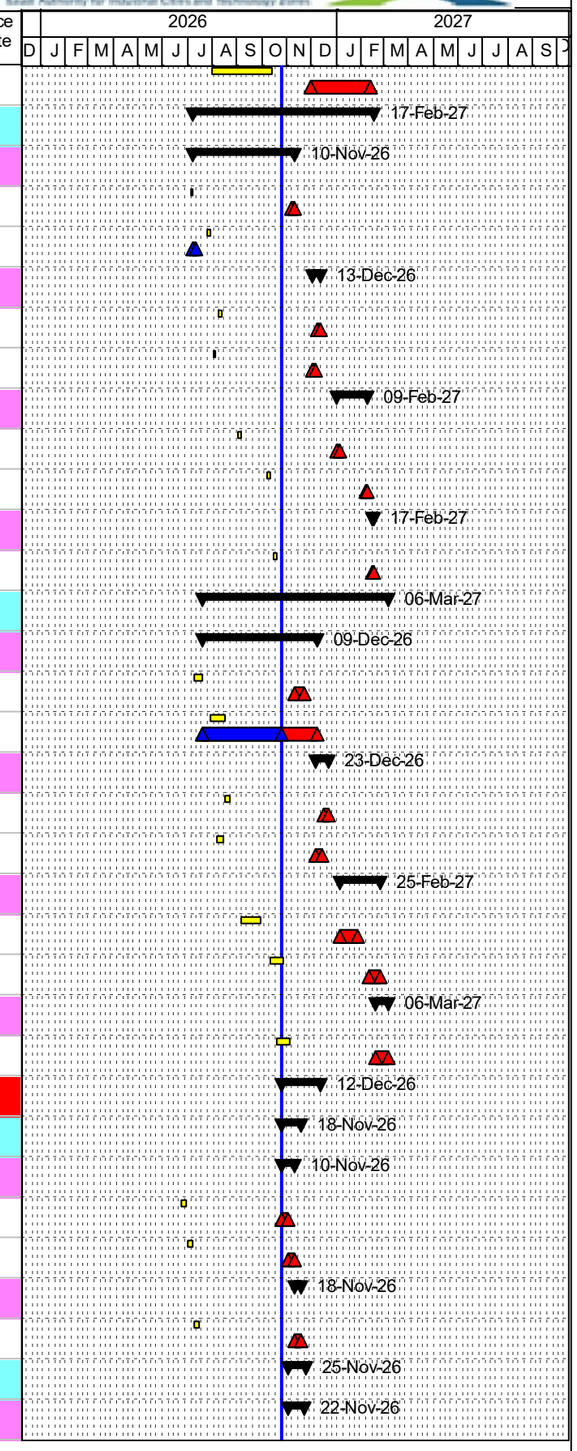


Primary Baseline | Actual Work | Summary
Remaining Work | Baseline Milestone
Critical Remaining Work | Milestone

Date	Revision	Checked	Approved
26-Oct-26	Third Industrial City		

Development of the Technology City in Dharan Project
BL-Update 26-10-2026
WPR UPS LEVEL 5

Activity ID	Activity Name	Original Duration	Start	Finish	Budgeted Total Cost	Planned Value Cost	Earned Value Cost	Actual Total Cost	Schedule % Complete	Performance % Complete
PRO-SW-MF-100	Manufacturing of Main Line Pipes for Sewage Network	80	03-Nov-26	14-Nov-26	0	0	0	0	100%	0%
PRO-SW-MF-110	Manufacturing of Manholes for Sewage Network	80	11-Nov-26	22-Nov-26	0	0	0	0	100%	0%
Testing and Finishes		48	19-Nov-26	25-Nov-26	0	0	0	0	0%	0%
PRO-SW-MF-120	Manufacturing of Manhole Covers for Sewage Network	48	19-Nov-26	25-Nov-26	0	0	0	0	100%	0%
1st Material Delivery & Site Inspection		128	15-Nov-26	02-Dec-26	0	0	0	0	0%	0%
Main Line Sections		112	15-Nov-26	30-Nov-26	0	0	0	0	0%	0%
PRO-SW-1DL-100	1ST Material Delivery for Main Line Pipes of Sewage Network	32	15-Nov-26	18-Nov-26	0	0	0	0	100%	0%
PRO-SW-1DL-110	1ST Material Delivery for Manholes of Sewage Network	32	26-Nov-26	30-Nov-26	0	0	0	0	100%	0%
Testing and Finishes		16	01-Dec-26	02-Dec-26	0	0	0	0	0%	0%
PRO-SW-1DL-120	1ST Material Delivery for Manholes Covers of Sewage Network	16	01-Dec-26	02-Dec-26	0	0	0	0	100%	0%
Material Delivery & Site Inspection		80	01-Dec-26	12-Dec-26	0	0	0	0	0%	0%
Main Line Sections		80	01-Dec-26	12-Dec-26	0	0	0	0	0%	0%
PRO-R25-SW-DL-100	Material Delivery & Site Inspection of Main Line Pipes for Sewage Network	32	08-Dec-26	12-Dec-26	0	0	0	0	100%	0%
PRO-R25-SW-DL-110	Material Delivery & Site Inspection of Manholes for Sewage Network	32	01-Dec-26	05-Dec-26	0	0	0	0	100%	0%
Testing and Finishes		32	03-Dec-26	07-Dec-26	0	0	0	0	0%	0%
PRO-R25-SW-DL-120	Material Delivery & Site Inspection of Manholes Covers for Sewage Network	32	03-Dec-26	07-Dec-26	0	0	0	0	100%	0%
Treated Sewage Effluent (Tse)		416	26-Oct-26	24-Dec-26	0	0	0	0	0%	0%
Issuance of Purchase Orders		56	26-Oct-26	02-Nov-26	0	0	0	0	0%	0%
PRO-TSE-PO-120	Issuance of Purchase Order for Materials of Treated Sewage Effluent (Tse)	56	26-Oct-26	02-Nov-26	0	0	0	0	100%	0%
Manufacturing of Material		192	03-Nov-26	30-Nov-26	0	0	0	0	0%	0%
PRO-TSE-MF-120	Manufacturing of Materials for Treated Sewage Effluent (Tse)	192	03-Nov-26	30-Nov-26	0	0	0	0	100%	0%
1st Material Delivery & Site Inspection		56	01-Dec-26	08-Dec-26	0	0	0	0	0%	0%
PRO-TSE-1DL-120	1ST Material Delivery for Materials of Treated Sewage Effluent (Tse)	56	01-Dec-26	08-Dec-26	0	0	0	0	100%	0%
Material Delivery & Site Inspection		112	09-Dec-26	24-Dec-26	0	0	0	0	0%	0%
PRO-R25-TSE-DL-120	Material Delivery & Site Inspection of Materials for Treated Sewage Effluent (Tse)	112	09-Dec-26	24-Dec-26	0	0	0	0	100%	0%
Potable Water Network		2248	02-May-26 A	03-Apr-27	0	0	0	0	0%	0%
Issuance of Purchase Orders		1264	02-May-26 A	07-Nov-26	0	0	0	0	0%	0%
Main Line Sections		88	02-May-26 A	12-May-26 A	0	0	0	0	0%	0%
PRO-PW-PO-100	Issuance of Purchase Order for Main Line Pipes and Materials of Potable Water Network	88	02-May-26 A	12-May-26 A	0	0	0	0	100%	100%
PRO-PW-PO-110	Issuance of Purchase Order for Valves of Potable Water Network	88	02-May-26 A	12-May-26 A	0	0	0	0	100%	100%
Fire Hydrant		40	26-Oct-26	31-Oct-26	0	0	0	0	0%	0%
PRO-PW-PO-120	Issuance of Purchase Order for Fire Hydrants of Potable Water Network	40	26-Oct-26	31-Oct-26	0	0	0	0	100%	0%
Testing and Finishes		48	01-Nov-26	07-Nov-26	0	0	0	0	0%	0%
PRO-PW-PO-130	Issuance of Purchase Order for Surface Box of Potable Water Network	48	01-Nov-26	07-Nov-26	0	0	0	0	100%	0%

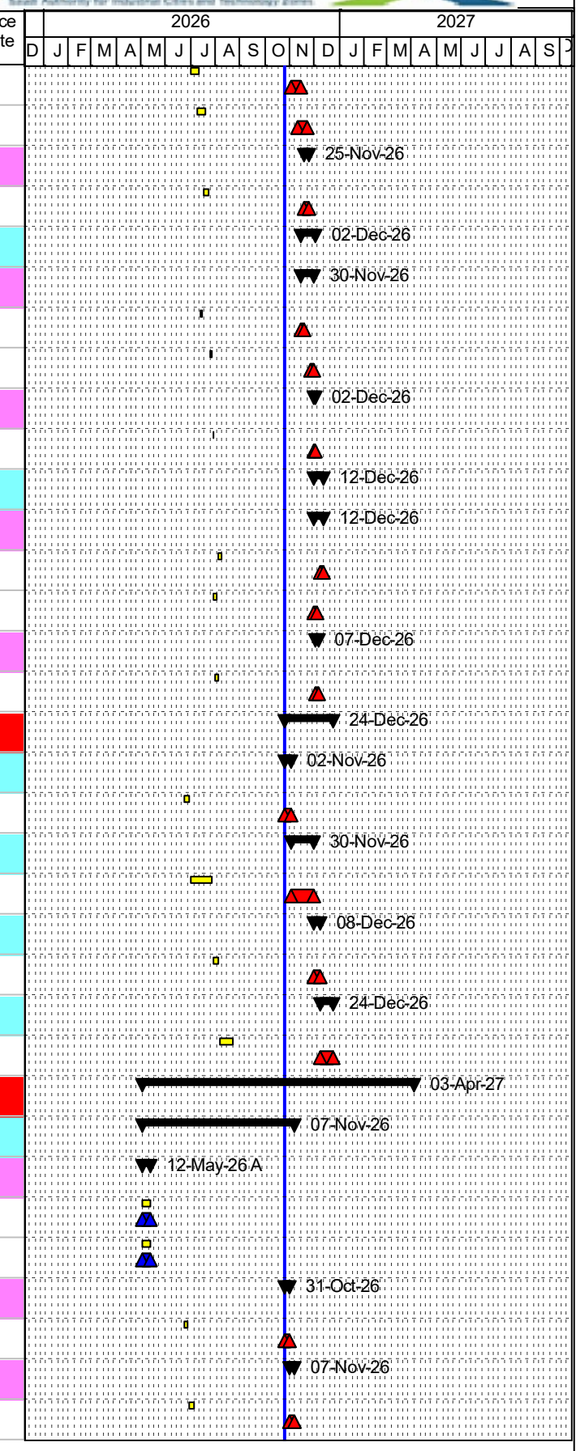


Primary Baseline | Actual Work | Summary
Remaining Work | Baseline Milestone
Critical Remaining Work | Milestone

Date	Revision	Checked	Approved
26-Oct-26	Third Industrial City		

Development of the Technology City in Dharan Project
BL-Update 26-10-2026
WPR UPS LEVEL 5


Activity ID	Activity Name	Original Duration	Start	Finish	Budgeted Total Cost	Planned Value Cost	Earned Value Cost	Actual Total Cost	Schedule % Complete	Performance % Complete
Manufacturing of Material		680	05-Jul-26 A	04-Jan-27	0	0	0	0	0%	0%
Main Line Sections		384	05-Jul-26 A	22-Nov-26	0	0	0	0	0%	0%
PRO-PW-MF-100	Manufacturing of Main Line Pipes and Materials for Potable Water Network	272	05-Jul-26 A	07-Jul-26 A	0	0	0	0	100%	100%
PRO-PW-MF-110	Manufacturing of Valves for Potable Water Network	192	26-Oct-26	22-Nov-26	0	0	0	0	100%	0%
Fire Hydrant		120	23-Nov-26	09-Dec-26	0	0	0	0	0%	0%
PRO-PW-MF-120	Manufacturing of Fire Hydrants for Potable Water Network	120	23-Nov-26	09-Dec-26	0	0	0	0	100%	0%
Testing and Finishes		400	08-Nov-26	04-Jan-27	0	0	0	0	0%	0%
PRO-PW-MF-130	Manufacturing for Surface Box of Potable Water Network	400	08-Nov-26	04-Jan-27	0	0	0	0	100%	0%
1st Material Delivery & Site Inspection		248	12-Jul-26 A	12-Jan-27	0	0	0	0	0%	0%
Main Line Sections		248	12-Jul-26 A	12-Jan-27	0	0	0	0	0%	0%
PRO-PW-1DL-100	1ST Material Delivery for Main Line Pipes and Materials of Potable Water Network	56	12-Jul-26 A	16-Jul-26 A	0	0	0	0	100%	100%
PRO-PW-1DL-110	1ST Material Delivery for Valves of Potable Water Network	56	05-Jan-27	12-Jan-27	0	0	0	0	100%	0%
Fire Hydrant		56	05-Jan-27	12-Jan-27	0	0	0	0	0%	0%
PRO-PW-1DL-120	1ST Material Delivery for Fire Hydrants of Potable Water Network	56	05-Jan-27	12-Jan-27	0	0	0	0	100%	0%
Testing and Finishes		56	05-Jan-27	12-Jan-27	0	0	0	0	0%	0%
PRO-PW-1DL-130	1ST Material Delivery for Finishes of Potable Water Network	56	05-Jan-27	12-Jan-27	0	0	0	0	100%	0%
Material Delivery & Site Inspection		720	10-Oct-26 A	03-Apr-27	0	0	0	0	0%	0%
Main Line Sections		360	10-Oct-26 A	06-Feb-27	0	0	0	0	0%	0%
PRO-R25-PW-DL-100	Material Delivery & Site Inspection of Main Line Pipes and Materials for Potable Water	168	10-Oct-26 A	09-Jan-27 A	0	0	0	0	100%	100%
PRO-R25-PW-DL-110	Material Delivery & Site Inspection of Valves for Potable Water Network	168	13-Jan-27	06-Feb-27	0	0	0	0	80.95%	0%
Fire Hydrant		48	13-Jan-27	19-Jan-27	0	0	0	0	0%	0%
PRO-R25-PW-DL-120	Material Delivery & Site Inspection of Fire Hydrants for Potable Water Network	48	13-Jan-27	19-Jan-27	0	0	0	0	100%	0%
Testing and Finishes		528	13-Jan-27	03-Apr-27	0	0	0	0	0%	0%
PRO-R25-PW-DL-130	Material Delivery & Site Inspection for Finishes of Potable Water Network	528	13-Jan-27	03-Apr-27	0	0	0	0	57.58%	0%
Irrigation Network		600	08-Nov-26	02-Feb-27	0	0	0	0	0%	0%
Issuance of Purchase Orders		72	08-Nov-26	17-Nov-26	0	0	0	0	0%	0%
Main Line Pipes		72	08-Nov-26	17-Nov-26	0	0	0	0	0%	0%
PRO-IR-PO-100	Issuance of Purchase Order for Main Line Pipes of Irrigation Network	40	08-Nov-26	12-Nov-26	0	0	0	0	100%	0%
PRO-IR-PO-110	Issuance of Purchase Order for Valves of Irrigation Network	32	14-Nov-26	17-Nov-26	0	0	0	0	100%	0%
Manufacturing of Material		336	14-Nov-26	31-Dec-26	0	0	0	0	0%	0%
Main Line Pipes		336	14-Nov-26	31-Dec-26	0	0	0	0	0%	0%
PRO-IR-MF-100	Manufacturing of Main Line Pipes for Irrigation Network	168	14-Nov-26	07-Dec-26	0	0	0	0	100%	0%
PRO-IR-MF-110	Manufacturing of Valves for Irrigation Network	168	08-Dec-26	31-Dec-26	0	0	0	0	100%	0%
1st Material Delivery & Site Inspection		224	08-Dec-26	09-Jan-27	0	0	0	0	0%	0%

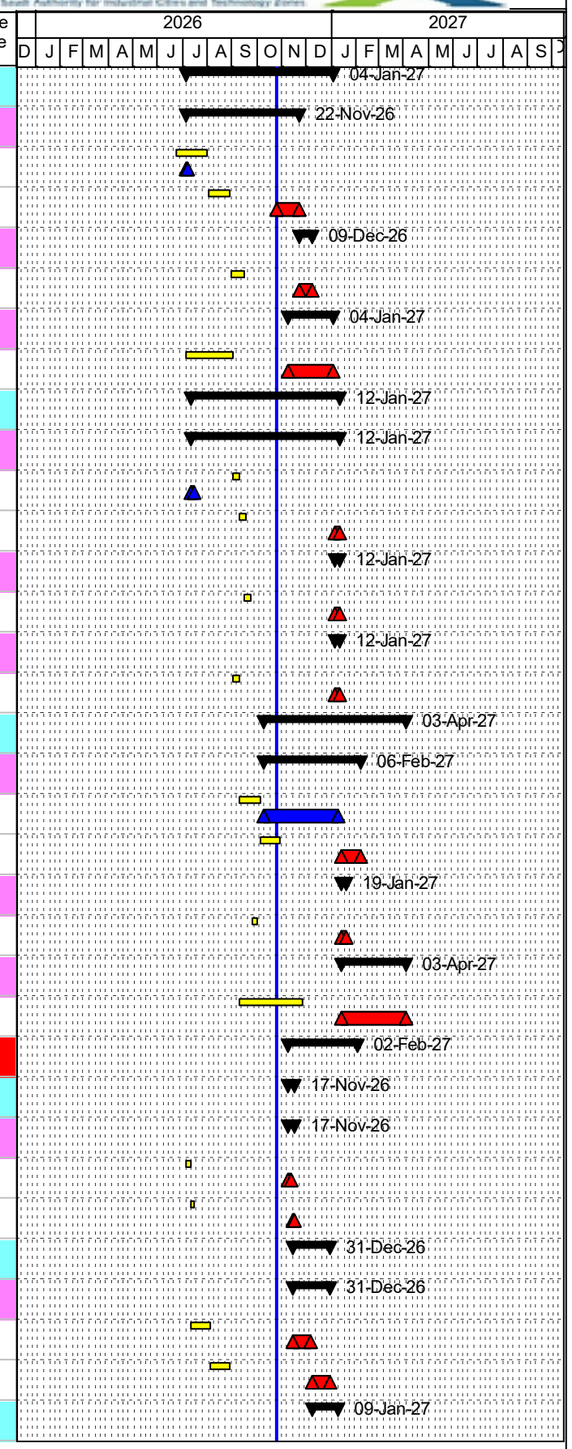

Primary Baseline | Actual Work | Summary
Remaining Work | Baseline Milestone
Critical Remaining Work | Milestone

Date	Revision	Checked	Approved
26-Oct-26	Third Industrial City		


Activity ID	Activity Name	Original Duration	Start	Finish	Budgeted Total Cost	Planned Value Cost	Earned Value Cost	Actual Total Cost	Schedule % Complete	Performance % Complete
Main Line Pipes		224	08-Dec-26	09-Jan-27	0	0	0	0	0%	0%
PRO-IR-1DL-100	1ST Material Delivery for Main Line Pipes of Irrigation Network	56	08-Dec-26	15-Dec-26	0	0	0	0	100%	0%
PRO-IR-1DL-110	1ST Material Delivery for Valves of Irrigation Network	56	02-Jan-27	09-Jan-27	0	0	0	0	100%	0%
Material Delivery & Site Inspection		336	16-Dec-26	02-Feb-27	0	0	0	0	0%	0%
Main Line Pipes		336	16-Dec-26	02-Feb-27	0	0	0	0	0%	0%
PRO-R25-IR-DL-100	Material Delivery & Site Inspection of Main Line Pipes for Irrigation Network	168	16-Dec-26	09-Jan-27	0	0	0	0	100%	0%
PRO-R25-IR-DL-110	Material Delivery & Site Inspection of Valves for Irrigation Network	168	10-Jan-27	02-Feb-27	0	0	0	0	100%	0%
Medium Voltage Network		528	18-Nov-26	02-Feb-27	0	0	0	0	0%	0%
Issuance of Purchase Orders		48	18-Nov-26	24-Nov-26	0	0	0	0	0%	0%
PRO-MV-PO-100	Issuance of Purchase Order for Medium Voltage Materials of Medium Voltage Network	48	18-Nov-26	24-Nov-26	0	0	0	0	100%	0%
Manufacturing of Material		168	25-Nov-26	19-Dec-26	0	0	0	0	0%	0%
PRO-MV-MF-100	Manufacturing of Medium Voltage Materials for Medium Voltage Network	168	25-Nov-26	19-Dec-26	0	0	0	0	100%	0%
1st Material Delivery & Site Inspection		56	20-Dec-26	27-Dec-26	0	0	0	0	0%	0%
PRO-MV-1DL-100	1ST Material Delivery for Medium Voltage Materials of Medium Voltage Network	56	20-Dec-26	27-Dec-26	0	0	0	0	100%	0%
Material Delivery & Site Inspection		168	10-Jan-27	02-Feb-27	0	0	0	0	0%	0%
PRO-MV-DL-100	Material Delivery & Site Inspection of Medium Voltage Materials for Medium Voltage Network	168	10-Jan-27	02-Feb-27	0	0	0	0	100%	0%
Low Voltage Network		1088	26-Oct-26	05-Apr-27	0	0	0	0	0%	0%
Issuance of Purchase Orders		224	26-Oct-26	26-Nov-26	0	0	0	0	0%	0%
Main Low Voltage Cables Works		56	26-Oct-26	02-Nov-26	0	0	0	0	0%	0%
PRO-LV-ML-PO-100	Issuance of Purchase Order for Main Low Voltage Cables of Low Voltage Network	56	26-Oct-26	02-Nov-26	0	0	0	0	100%	0%
Service Low Voltage Cables Works		56	26-Oct-26	02-Nov-26	0	0	0	0	0%	0%
PRO-LV-HC-PO-100	Issuance of Purchase Order for Service Low Voltage Cables of Low Voltage Network	56	26-Oct-26	02-Nov-26	0	0	0	0	100%	0%
Distribution Pillar Works		112	03-Nov-26	18-Nov-26	0	0	0	0	0%	0%
PRO-LV-DP-PO-100	Issuance of Purchase Order for Distribution Pillars of Low Voltage Network	56	03-Nov-26	10-Nov-26	0	0	0	0	100%	0%
PRO-LV-DP-PO-110	Issuance of Purchase Order for Low Voltage Earthing of Low Voltage Network	56	11-Nov-26	18-Nov-26	0	0	0	0	100%	0%
Termination and Testing Works		56	19-Nov-26	26-Nov-26	0	0	0	0	0%	0%
PRO-LV-TT-PO-100	Issuance of Purchase Order for Cable Lugs of Low Voltage Network	56	19-Nov-26	26-Nov-26	0	0	0	0	100%	0%
Manufacturing of Material		728	03-Nov-26	16-Feb-27	0	0	0	0	0%	0%
Main Low Voltage Cables Works		240	03-Nov-26	07-Dec-26	0	0	0	0	0%	0%
PRO-LV-ML-MF-100	Manufacturing of Main Low Voltage Cables for Low Voltage Network	240	03-Nov-26	07-Dec-26	0	0	0	0	100%	0%
Service Low Voltage Cables Works		240	03-Nov-26	07-Dec-26	0	0	0	0	0%	0%
PRO-LV-HC-MF-100	Manufacturing of Service Low Voltage Cables for Low Voltage Network	240	03-Nov-26	07-Dec-26	0	0	0	0	100%	0%
Distribution Pillar Works		376	11-Nov-26	04-Jan-27	0	0	0	0	0%	0%
PRO-LV-DP-MF-100	Manufacturing of Distribution Pillars for Low Voltage Network	320	11-Nov-26	27-Dec-26	0	0	0	0	100%	0%

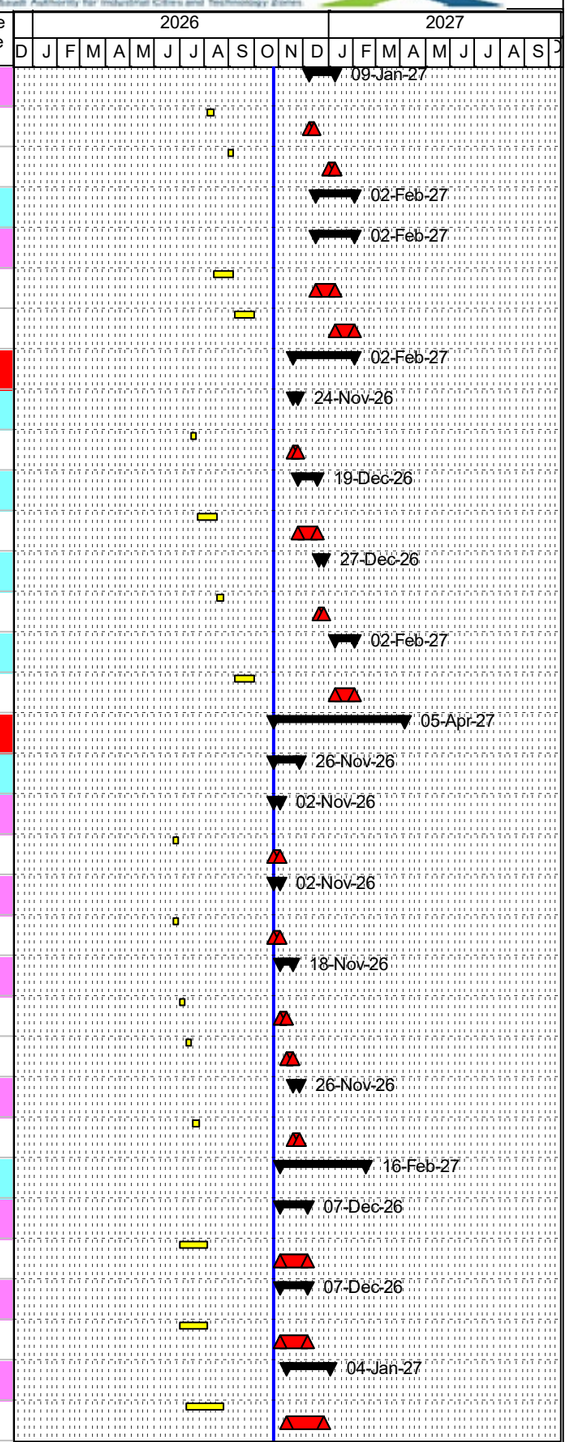

Primary Baseline | Actual Work | Summary
Remaining Work | Baseline Milestone
Critical Remaining Work | Milestone

Date	Revision	Checked	Approved
26-Oct-26	Third Industrial City		


Activity ID	Activity Name	Original Duration	Start	Finish	Budgeted Total Cost	Planned Value Cost	Earned Value Cost	Actual Total Cost	Schedule % Complete	Performance % Complete
PRO-LV-DP-MF-110	Manufacturing of Low Voltage Earthing for Low Voltage Network	320	19-Nov-26	04-Jan-27	0	0	0	0	100%	0%
Termination and Testing Works		560	28-Nov-26	16-Feb-27	0	0	0	0	0%	0%
PRO-LV-TT-MF-100	Manufacturing of Cable Lugs for Low Voltage Network	560	28-Nov-26	16-Feb-27	0	0	0	0	100%	0%
1st Delivery of Material to Site		496	08-Dec-26	17-Feb-27	0	0	0	0	0%	0%
Main Low Voltage Cables Works		272	08-Dec-26	16-Jan-27	0	0	0	0	0%	0%
PRO-LV-ML-1DL-100	1ST Material Delivery for Main Low Voltage Cables of Low Voltage Network	272	08-Dec-26	16-Jan-27	0	0	0	0	100%	0%
Service Low Voltage Cables Works		56	17-Jan-27	24-Jan-27	0	0	0	0	0%	0%
PRO-LV-HC-1DL-100	1ST Material Delivery for Service Low Voltage Cables of Low Voltage Network	56	17-Jan-27	24-Jan-27	0	0	0	0	100%	0%
Distribution Pillar Works		112	25-Jan-27	09-Feb-27	0	0	0	0	0%	0%
PRO-LV-DP-1DL-100	1ST Material Delivery for Distribution Pillars of Low Voltage Network	56	25-Jan-27	01-Feb-27	0	0	0	0	100%	0%
PRO-LV-DP-1DL-110	1ST Material Delivery for Low Voltage Earthing of Low Voltage Network	56	02-Feb-27	09-Feb-27	0	0	0	0	100%	0%
Termination and Testing Works		56	10-Feb-27	17-Feb-27	0	0	0	0	0%	0%
PRO-LV-TT-1DL-100	1ST Material Delivery for Cable Lugs of Low Voltage Network	56	10-Feb-27	17-Feb-27	0	0	0	0	100%	0%
Delivery of Material to Site		520	17-Jan-27	05-Apr-27	0	0	0	0	0%	0%
Main Low Voltage Cables Works		56	17-Jan-27	24-Jan-27	0	0	0	0	0%	0%
PRO-LV-ML-DL-100	Material Delivery of Main Low Voltage Cables for Low Voltage Network	56	17-Jan-27	24-Jan-27	0	0	0	0	100%	0%
Service Low Voltage Cables Works		168	25-Jan-27	17-Feb-27	0	0	0	0	0%	0%
PRO-LV-HC-DL-100	Material Delivery of Service Low Voltage Cables for Low Voltage Network	168	25-Jan-27	17-Feb-27	0	0	0	0	100%	0%
Distribution Pillar Works		160	17-Feb-27	15-Mar-27	0	0	0	0	0%	0%
PRO-LV-DP-DL-100	Material Delivery of Distribution Pillars for Low Voltage Network	152	18-Feb-27	15-Mar-27	0	0	0	0	36.84%	0%
PRO-LV-DP-DL-120	Material Delivery of Low Voltage Earthing for Low Voltage Network	160	17-Feb-27	15-Mar-27	0	0	0	0	40%	0%
Termination and Testing Works		144	16-Mar-27	05-Apr-27	0	0	0	0	0%	0%
PRO-LV-TT-DL-100	Material Delivery of Cable Lugs for Low Voltage Network	144	16-Mar-27	05-Apr-27	0	0	0	0	0%	0%
Street Lighting Network		1040	19-Nov-26	22-Apr-27	0	0	0	0	0%	0%
Issuance of Purchase Orders		136	19-Nov-26	08-Dec-26	0	0	0	0	0%	0%
Cabling Works		40	19-Nov-26	24-Nov-26	0	0	0	0	0%	0%
PRO-SL-PO-100	Issuance of Purchase Order for Lighting Cables of Street Lighting Network	40	19-Nov-26	24-Nov-26	0	0	0	0	100%	0%
Lighting Poles Works		40	19-Nov-26	24-Nov-26	0	0	0	0	0%	0%
PRO-SL-PO-110	Issuance of Purchase Order for Lighting Poles Foundations of Street Lighting Network	40	19-Nov-26	24-Nov-26	0	0	0	0	100%	0%
PRO-SL-PO-120	Issuance of Purchase Order for Lighting Poles of Street Lighting Network	40	19-Nov-26	24-Nov-26	0	0	0	0	100%	0%
PRO-SL-PO-140	Issuance of Purchase Order for Lighting Fixtures of Street Lighting Network	40	19-Nov-26	24-Nov-26	0	0	0	0	100%	0%
Distribution Panel Board		48	19-Nov-26	25-Nov-26	0	0	0	0	0%	0%
PRO-SL-PO-160	Issuance of Purchase Order for Distrubution Panel Boards of Street Lighting Network	48	19-Nov-26	25-Nov-26	0	0	0	0	100%	0%
Termination and Testing Works		56	25-Nov-26	02-Dec-26	0	0	0	0	0%	0%

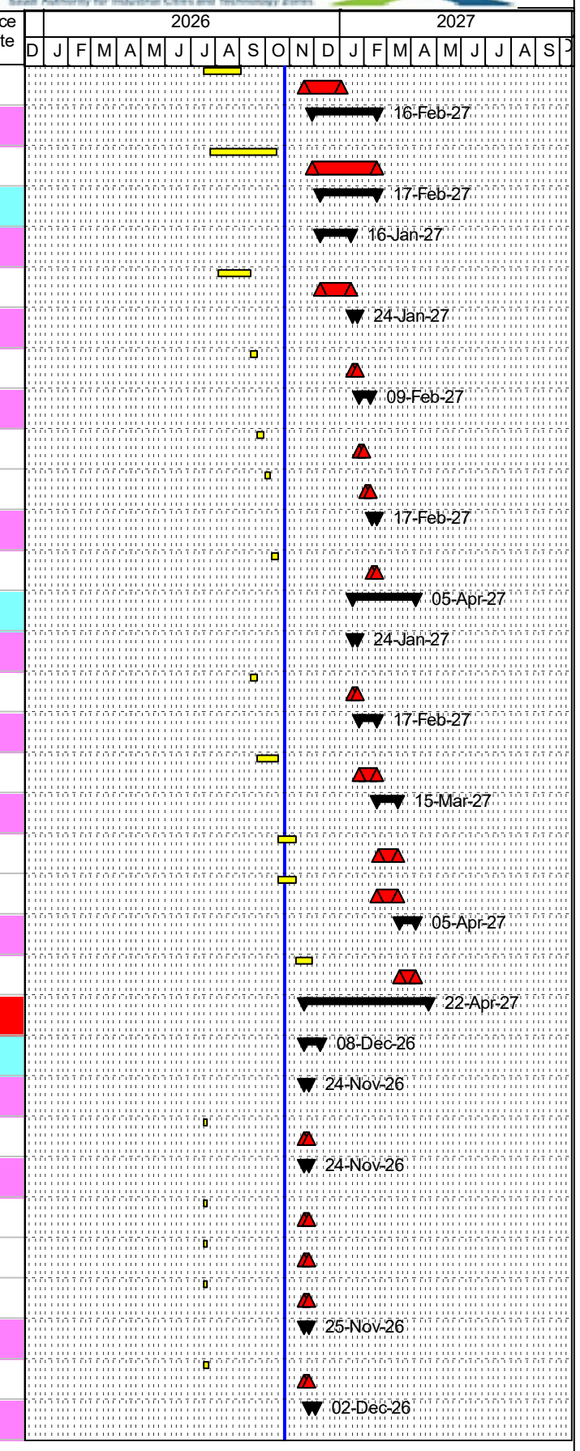

Primary Baseline | Actual Work | Summary
Remaining Work | Baseline Milestone
Critical Remaining Work | Milestone

Date	Revision	Checked	Approved
26-Oct-26	Third Industrial City		

Activity ID	Activity Name	Original Duration	Start	Finish	Budgeted Total Cost	Planned Value Cost	Earned Value Cost	Actual Total Cost	Schedule % Complete	Performance % Complete
PRO-SL-PO-130	Issuance of Purchase Order for Fuse Boxes of Street Lighting Network	48	26-Nov-26	02-Dec-26	0	0	0	0	100%	0%
PRO-SL-PO-170	Issuance of Purchase Order for Cable Lugs of Street Lighting Network	48	25-Nov-26	01-Dec-26	0	0	0	0	100%	0%
Earthing System Works		48	02-Dec-26	08-Dec-26	0	0	0	0	0%	0%
PRO-SL-PO-150	Issuance of Purchase Order for Lighting Earthing of Street Lighting Network	48	02-Dec-26	08-Dec-26	0	0	0	0	100%	0%
Manufacturing of Material		784	25-Nov-26	22-Mar-27	0	0	0	0	0%	0%
Cabling Works		160	25-Nov-26	17-Dec-26	0	0	0	0	0%	0%
PRO-SL-MF-100	Manufacturing of Lighting Cables for Street Lighting Network	160	25-Nov-26	17-Dec-26	0	0	0	0	100%	0%
Lighting Poles Works		168	19-Dec-26	11-Jan-27	0	0	0	0	0%	0%
PRO-SL-MF-110	Manufacturing of Lighting Poles Foundations for Street Lighting Network	168	19-Dec-26	11-Jan-27	0	0	0	0	100%	0%
PRO-SL-MF-120	Manufacturing of Lighting Poles for Street Lighting Network	168	19-Dec-26	11-Jan-27	0	0	0	0	100%	0%
PRO-SL-MF-140	Manufacturing of Lighting Fixtures for Street Lighting Network	168	19-Dec-26	11-Jan-27	0	0	0	0	100%	0%
Distribution Panel Board		240	12-Jan-27	15-Feb-27	0	0	0	0	0%	0%
PRO-SL-MF-160	Manufacturing of Distrubution Panel Boards for Street Lighting Network	240	12-Jan-27	15-Feb-27	0	0	0	0	100%	0%
Termination and Testing Works		728	03-Dec-26	22-Mar-27	0	0	0	0	0%	0%
PRO-SL-MF-130	Manufacturing of Fuse Boxes for Street Lighting Network	560	03-Dec-26	22-Feb-27	0	0	0	0	100%	0%
PRO-SL-MF-170	Manufacturing of Cable Lugs for Street Lighting Network	168	23-Feb-27	22-Mar-27	0	0	0	0	14.29%	0%
Earthing System Works		320	09-Dec-26	24-Jan-27	0	0	0	0	0%	0%
PRO-SL-MF-150	Manufacturing of Lighting Earthing for Street Lighting Network	320	09-Dec-26	24-Jan-27	0	0	0	0	100%	0%
1st Material Delivery & Site Inspection		720	19-Dec-26	05-Apr-27	0	0	0	0	0%	0%
Cabling Works		48	19-Dec-26	24-Dec-26	0	0	0	0	0%	0%
PRO-SL-1DL-100	1ST Material Delivery for Lighting Cables of Street Lighting Network	48	19-Dec-26	24-Dec-26	0	0	0	0	100%	0%
Lighting Poles Works		144	12-Jan-27	01-Feb-27	0	0	0	0	0%	0%
PRO-SL-1DL-110	1ST Material Delivery for Lighting Poles Foundations of Street Lighting Network	48	12-Jan-27	18-Jan-27	0	0	0	0	100%	0%
PRO-SL-1DL-120	1ST Material Delivery for Lighting Poles of Street Lighting Network	48	19-Jan-27	25-Jan-27	0	0	0	0	100%	0%
PRO-SL-1DL-140	1ST Material Delivery for Lighting Fixtures of Street Lighting Network	48	26-Jan-27	01-Feb-27	0	0	0	0	100%	0%
Distribution Panel Board		48	16-Feb-27	22-Feb-27	0	0	0	0	0%	0%
PRO-SL-1DL-160	1ST Material Delivery for Distrubution Panel Boards of Street Lighting Network	48	16-Feb-27	22-Feb-27	0	0	0	0	100%	0%
Termination and Testing Works		216	23-Feb-27	29-Mar-27	0	0	0	0	0%	0%
PRO-SL-1DL-130	1ST Material Delivery for Fuse Boxes of Street Lighting Network	48	23-Feb-27	01-Mar-27	0	0	0	0	50%	0%
PRO-SL-1DL-170	1ST Material Delivery for Cable Lugs of Street Lighting Network	48	23-Mar-27	29-Mar-27	0	0	0	0	0%	0%
Earthing System Works		48	30-Mar-27	05-Apr-27	0	0	0	0	0%	0%
PRO-SL-1DL-150	1ST Material Delivery for Lighting Earthing of Street Lighting Network	48	30-Mar-27	05-Apr-27	0	0	0	0	0%	0%
Material Delivery & Site Inspection		792	26-Dec-26	22-Apr-27	0	0	0	0	0%	0%
Cabling Works		168	26-Dec-26	18-Jan-27	0	0	0	0	0%	0%

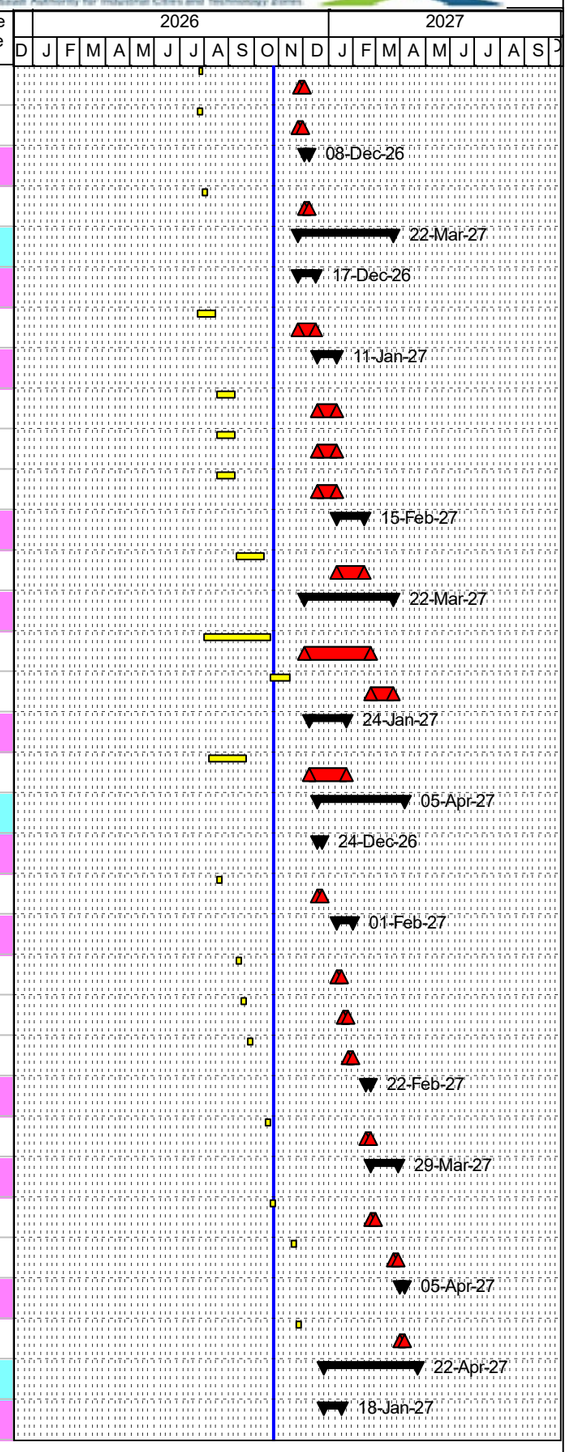


Primary Baseline | Actual Work | Summary
Remaining Work | Baseline Milestone
Critical Remaining Work | Milestone

Date	Revision	Checked	Approved
26-Oct-26	Third Industrial City		

Development of the Technology City in Dharan Project
BL-Update 26-10-2026
WPR UPS LEVEL 5


Activity ID	Activity Name	Original Duration	Start	Finish	Budgeted Total Cost	Planned Value Cost	Earned Value Cost	Actual Total Cost	Schedule % Complete	Performance % Complete
PRO-R25-SL-DL-100	Material Delivery & Site Inspection of Lighting Cables for Street Lighting Network	168	26-Dec-26	18-Jan-27	0	0	0	0	100%	0%
Lighting Poles Works		336	12-Jan-27	01-Mar-27	0	0	0	0	0%	0%
PRO-R25-SL-DL-110	Material Delivery & Site Inspection of Lighting Poles Foundations for Street Lighting Network	168	12-Jan-27	04-Feb-27	0	0	0	0	100%	0%
PRO-R25-SL-DL-120	Material Delivery & Site Inspection of Lighting Poles for Street Lighting Network	168	06-Feb-27	01-Mar-27	0	0	0	0	85.71%	0%
PRO-R25-SL-DL-140	Material Delivery & Site Inspection of Lighting Fixtures for Street Lighting Network	168	06-Feb-27	01-Mar-27	0	0	0	0	85.71%	0%
Distribution Panel Board		168	02-Mar-27	29-Mar-27	0	0	0	0	0%	0%
PRO-R25-SL-DL-160	Material Delivery & Site Inspection of Distrubution Panel Boards for Street Lighting	168	02-Mar-27	29-Mar-27	0	0	0	0	0%	0%
Termination and Testing Works		168	30-Mar-27	22-Apr-27	0	0	0	0	0%	0%
PRO-R25-SL-DL-130	Material Delivery & Site Inspection of Fuse Boxes for Street Lighting Network	168	30-Mar-27	22-Apr-27	0	0	0	0	0%	0%
PRO-R25-SL-DL-170	Material Delivery & Site Inspection of Cable Lugs for Street Lighting Network	168	30-Mar-27	22-Apr-27	0	0	0	0	0%	0%
Earthing System Works		168	30-Mar-27	22-Apr-27	0	0	0	0	0%	0%
PRO-R25-SL-DL-150	Material Delivery & Site Inspection of Lighting Earthing for Street Lighting Network	168	30-Mar-27	22-Apr-27	0	0	0	0	0%	0%
Telecom and Light Current Network		744	02-Dec-26	23-Mar-27	0	0	0	0	0%	0%
Issuance of Purchase Orders		160	02-Dec-26	24-Dec-26	0	0	0	0	0%	0%
Ducts Works		56	02-Dec-26	09-Dec-26	0	0	0	0	0%	0%
PRO-TE-PO-100	Issuance of Purchase Order for Ducts forTelecom Network	56	02-Dec-26	09-Dec-26	0	0	0	0	100%	0%
Manholes Works		56	02-Dec-26	09-Dec-26	0	0	0	0	0%	0%
PRO-TE-PO-110	Issuance of Purchase Order for Manholes forTelecom Network	56	02-Dec-26	09-Dec-26	0	0	0	0	100%	0%
CCTV, Telephone, MSN, ACs System Works		160	02-Dec-26	24-Dec-26	0	0	0	0	0%	0%
PRO-CTV-PO-100	Issuance of Purchase Order for Civil and Finishes Works of CCTV Complete System	160	02-Dec-26	24-Dec-26	0	0	0	0	100%	0%
Manufacturing of Material		560	10-Dec-26	01-Mar-27	0	0	0	0	0%	0%
Ducts Works		160	10-Dec-26	02-Jan-27	0	0	0	0	0%	0%
PRO-TE-MF-100	Manufacturing of Ducts for Telecom Network	160	10-Dec-26	02-Jan-27	0	0	0	0	100%	0%
Manholes Works		160	03-Jan-27	25-Jan-27	0	0	0	0	0%	0%
PRO-TE-MF-110	Manufacturing of Manholes for Telecom Network	160	03-Jan-27	25-Jan-27	0	0	0	0	100%	0%
CCTV, Telephone, MSN, ACs System Works		240	26-Jan-27	01-Mar-27	0	0	0	0	0%	0%
PRO-CTV-MF-100	Manufacturing of Civil and Finishes Works for CCTV Complete System	240	26-Jan-27	01-Mar-27	0	0	0	0	90%	0%
1st Material Delivery & Site Inspection		448	03-Jan-27	08-Mar-27	0	0	0	0	0%	0%
Ducts Works		48	03-Jan-27	09-Jan-27	0	0	0	0	0%	0%
PRO-TE-1DL-100	1ST Material Delivery for Ducts of Telecom Network	48	03-Jan-27	09-Jan-27	0	0	0	0	100%	0%
Manholes Works		48	26-Jan-27	01-Feb-27	0	0	0	0	0%	0%
PRO-TE-1DL-110	1ST Material Delivery for Manholes of Telecom Network	48	26-Jan-27	01-Feb-27	0	0	0	0	100%	0%
CCTV, Telephone, MSN, ACs System Works		48	02-Mar-27	08-Mar-27	0	0	0	0	0%	0%
PRO-CTV-1DL-100	1ST Material Delivery for Civil and Finishes Works of CCTV Complete System	48	02-Mar-27	08-Mar-27	0	0	0	0	0%	0%

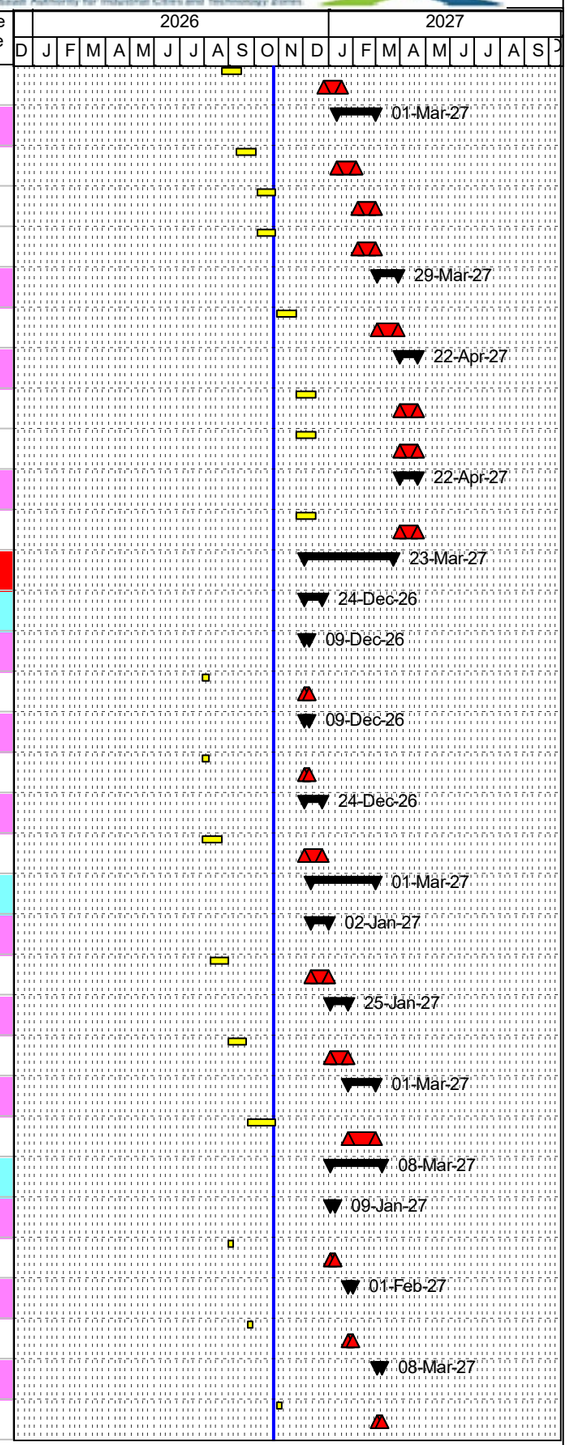

Primary Baseline | Actual Work | Summary
Remaining Work | Baseline Milestone
Critical Remaining Work | Milestone

Date	Revision	Checked	Approved
26-Oct-26	Third Industrial City		


Activity ID	Activity Name	Original Duration	Start	Finish	Budgeted Total Cost	Planned Value Cost	Earned Value Cost	Actual Total Cost	Schedule % Complete	Performance % Complete
Material Delivery & Site Inspection		480	10-Jan-27	23-Mar-27	0	0	0	0	0%	0%
Ducts Works		120	10-Jan-27	26-Jan-27	0	0	0	0	0%	0%
PRO-R25-TE-DL-100	Material Delivery & Site Inspection for Ducts of Telecom Network	120	10-Jan-27	26-Jan-27	0	0	0	0	100%	0%
Manholes Works		120	02-Feb-27	18-Feb-27	0	0	0	0	0%	0%
PRO-R25-TE-DL-110	Material Delivery & Site Inspection of Manholes for Telecom Network	120	02-Feb-27	18-Feb-27	0	0	0	0	100%	0%
CCTV, Telephone, MSN, ACs System Works		80	13-Mar-27	23-Mar-27	0	0	0	0	0%	0%
PRO-R25-CTV-DL-100	Material Delivery & Site Inspection of for Civil and Finishes Works of CCTV Complete	80	13-Mar-27	23-Mar-27	0	0	0	0	0%	0%
Road Works		1272	26-Oct-26	02-May-27	0	0	0	0	0%	0%
Issuance of Purchase Orders		336	26-Oct-26	13-Dec-26	0	0	0	0	0%	0%
Road Works		336	26-Oct-26	13-Dec-26	0	0	0	0	0%	0%
PRO-RD-PO-100	Issuance of Purchase Order for Subgrade of Road Works	56	26-Oct-26	02-Nov-26	0	0	0	0	100%	0%
PRO-RD-PO-110	Issuance of Purchase Order for Aggregate Base Course of Road Works	56	03-Nov-26	10-Nov-26	0	0	0	0	100%	0%
PRO-RD-PO-120	Issuance of Purchase Order for Prime Coat of Road Works	56	11-Nov-26	18-Nov-26	0	0	0	0	100%	0%
PRO-RD-PO-130	Issuance of Purchase Order for Asphaltic Base Course Laver of Road Works	56	19-Nov-26	26-Nov-26	0	0	0	0	100%	0%
PRO-RD-PO-180	Issuance of Purchase Order for Asphaltic Wearing Course Laver for Roads Network	56	28-Nov-26	05-Dec-26	0	0	0	0	100%	0%
PRO-RD-PO-190	Issuance of Purchase Order for Tack Coat Layer for Roads Network	56	06-Dec-26	13-Dec-26	0	0	0	0	100%	0%
Pavement Works		112	11-Nov-26	26-Nov-26	0	0	0	0	0%	0%
PRO-RD-PO-140	Issuance of Purchase Order for Interlock Tiles of Landscaping	56	11-Nov-26	18-Nov-26	0	0	0	0	100%	0%
PRO-RD-PO-150	Issuance of Purchase Order for Curbstones of Landscaping	56	19-Nov-26	26-Nov-26	0	0	0	0	100%	0%
Traffic Signs Boards and Roads Marking		112	28-Nov-26	13-Dec-26	0	0	0	0	0%	0%
PRO-RD-PO-160	Issuance of Purchase Order for Traffic Signs Boards of Road Works	56	28-Nov-26	05-Dec-26	0	0	0	0	100%	0%
PRO-RD-PO-170	Issuance of Purchase Order for Road Markings of Road Works	56	06-Dec-26	13-Dec-26	0	0	0	0	100%	0%
Manufacturing of Material		920	03-Nov-26	20-Mar-27	0	0	0	0	0%	0%
Road Works		720	03-Nov-26	15-Feb-27	0	0	0	0	0%	0%
PRO-RD-MF-100	Manufacturing of Subgrade for Road Works	80	03-Nov-26	14-Nov-26	0	0	0	0	100%	0%
PRO-RD-MF-110	Manufacturing of Aggregate Base Course for Road Works	160	15-Nov-26	07-Dec-26	0	0	0	0	100%	0%
PRO-RD-MF-120	Manufacturing of Prime Coat for Road Works	160	08-Dec-26	30-Dec-26	0	0	0	0	100%	0%
PRO-RD-MF-130	Manufacturing of Asphaltic Base Course Layer for Road Works	160	31-Dec-26	23-Jan-27	0	0	0	0	100%	0%
PRO-RD-MF-180	Manufacturing of Asphaltic Wearing Course Layer for Roads Network	160	24-Jan-27	15-Feb-27	0	0	0	0	100%	0%
PRO-RD-MF-190	Manufacturing of Tack Coat Layer for Roads Network	400	14-Dec-26	09-Feb-27	0	0	0	0	100%	0%
Pavement Works		168	10-Feb-27	06-Mar-27	0	0	0	0	0%	0%
PRO-RD-MF-140	Manufacturing of Interlock Tiles for Landscaping	168	10-Feb-27	06-Mar-27	0	0	0	0	66.67%	0%
PRO-RD-MF-150	Manufacturing of Curbstones for Landscaping	160	10-Feb-27	04-Mar-27	0	0	0	0	70%	0%
Traffic Signs Boards and Roads Marking		696	06-Dec-26	20-Mar-27	0	0	0	0	0%	0%

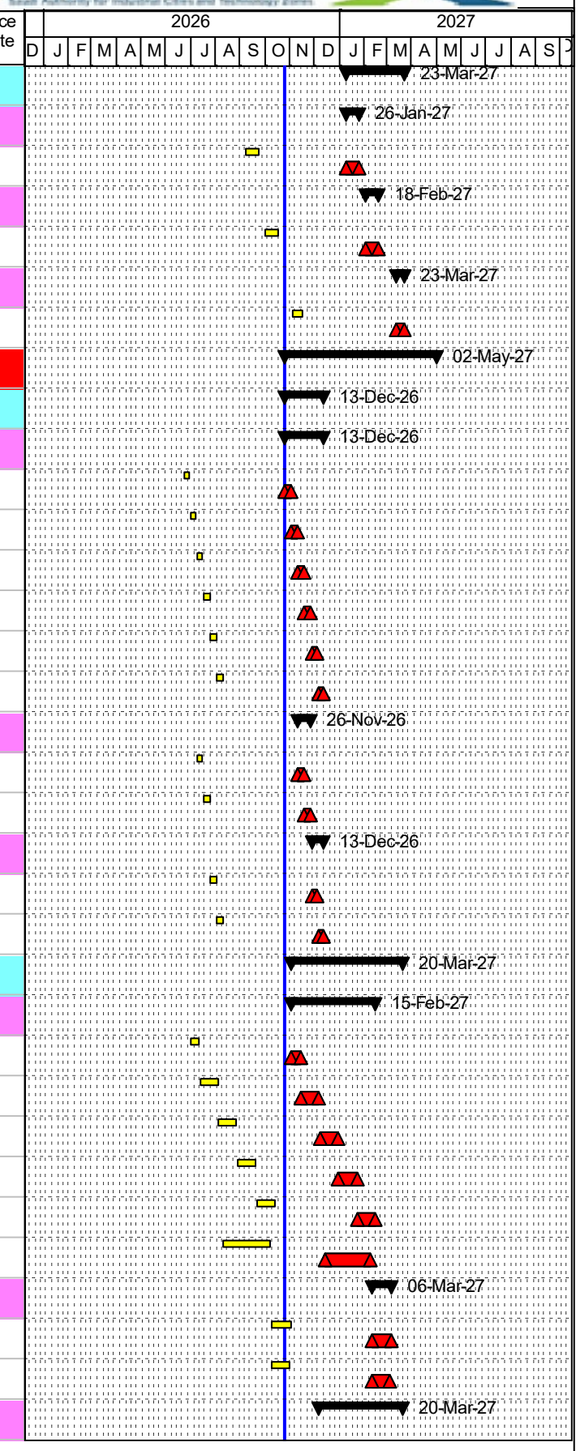

Primary Baseline | Actual Work | Summary
Remaining Work | Baseline Milestone
Critical Remaining Work | Milestone

Date	Revision	Checked	Approved
26-Oct-26	Third Industrial City		

Activity ID	Activity Name	Original Duration	Start	Finish	Budgeted Total Cost	Planned Value Cost	Earned Value Cost	Actual Total Cost	Schedule % Complete	Performance % Complete
PRO-RD-MF-160	Manufacturing of Traffic Signs Boards for Road Works	640	06-Dec-26	08-Mar-27	0	0	0	0	88.75%	0%
PRO-RD-MF-170	Manufacturing of Road Markings for Road Works	640	14-Dec-26	20-Mar-27	0	0	0	0	80%	0%
1st Material Delivery & Site Inspection		992	15-Nov-26	11-Apr-27	0	0	0	0	0%	0%
Road Works		752	15-Nov-26	03-Mar-27	0	0	0	0	0%	0%
PRO-RD-1DL-100	1ST Material Delivery for Subgrade of Road Works	56	15-Nov-26	22-Nov-26	0	0	0	0	100%	0%
PRO-RD-1DL-110	1ST Material Delivery for Aggregate Base Course of Road Works	56	08-Dec-26	15-Dec-26	0	0	0	0	100%	0%
PRO-RD-1DL-120	1ST Material Delivery for Prime Coat of Road Works	120	31-Dec-26	17-Jan-27	0	0	0	0	100%	0%
PRO-RD-1DL-130	1ST Material Delivery for Asphaltic Base Course Layer of Road Works	56	24-Jan-27	31-Jan-27	0	0	0	0	100%	0%
PRO-RD-1DL-180	1ST Material Delivery for Asphaltic Wearing Course Layer for Roads Network	56	16-Feb-27	23-Feb-27	0	0	0	0	100%	0%
PRO-RD-1DL-190	1ST Material Delivery for Tack Coat Layer for Roads Network	56	24-Feb-27	03-Mar-27	0	0	0	0	28.57%	0%
Pavement Works		112	07-Mar-27	25-Mar-27	0	0	0	0	0%	0%
PRO-RD-1DL-140	1ST Material Delivery for Interlock Tiles of Landscaping	56	07-Mar-27	17-Mar-27	0	0	0	0	0%	0%
PRO-RD-1DL-150	1ST Material Delivery for Curbstones of Landscaping	56	18-Mar-27	25-Mar-27	0	0	0	0	0%	0%
Traffic Signs Boards and Roads Marking		112	27-Mar-27	11-Apr-27	0	0	0	0	0%	0%
PRO-RD-1DL-160	1ST Material Delivery for Traffic Signs Boards of Road Works	56	04-Apr-27	11-Apr-27	0	0	0	0	0%	0%
PRO-RD-1DL-170	1ST Material Delivery for Road Markings of Road Works	56	27-Mar-27	03-Apr-27	0	0	0	0	0%	0%
Material Delivery & Site Inspection		1080	23-Nov-26	02-May-27	0	0	0	0	0%	0%
Pre-Bituminous Construction		336	23-Nov-26	10-Jan-27	0	0	0	0	0%	0%
PRO-R25-RD-DL-100	Material Delivery & Site Inspection for Subgrade of Road Works	168	23-Nov-26	16-Dec-26	0	0	0	0	100%	0%
PRO-R25-RD-DL-110	Material Delivery & Site Inspection for Aggregate Base Course of Road Works	168	17-Dec-26	10-Jan-27	0	0	0	0	100%	0%
Bituminous Construction		432	18-Jan-27	24-Mar-27	0	0	0	0	0%	0%
PRO-R25-RD-DL-160	Material Delivery & Site Inspection for Prime Coat Layer of Road Works	88	18-Jan-27	30-Jan-27	0	0	0	0	100%	0%
PRO-R25-RD-DL-170	Material Delivery & Site Inspection for Asphaltic Base Course Layer of Road Works	88	01-Feb-27	13-Feb-27	0	0	0	0	100%	0%
PRO-RD-DL-200	Material Delivery for Asphaltic Wearing Course Layer for Roads Network	88	24-Feb-27	08-Mar-27	0	0	0	0	18.18%	0%
PRO-RD-DL-210	Material Delivery for Tack Coat Layer for Roads Network	88	13-Mar-27	24-Mar-27	0	0	0	0	0%	0%
Pavement Works		176	25-Mar-27	19-Apr-27	0	0	0	0	0%	0%
PRO-R25-RD-DL-120	Material Delivery & Site Inspection of Interlock Tiles for Landscaping	88	25-Mar-27	06-Apr-27	0	0	0	0	0%	0%
PRO-R25-RD-DL-130	Material Delivery & Site Inspection of Curbstones for Landscaping	88	07-Apr-27	19-Apr-27	0	0	0	0	0%	0%
Traffic Signs Boards and Roads Marking		176	07-Apr-27	02-May-27	0	0	0	0	0%	0%
PRO-R25-RD-DL-140	Material Delivery & Site Inspection of Traffic Signs Boards For Road Works	88	20-Apr-27	02-May-27	0	0	0	0	0%	0%
PRO-R25-RD-DL-150	Material Delivery & Site Inspection of Road Markings For Road Works	88	07-Apr-27	19-Apr-27	0	0	0	0	0%	0%
Superstructure Works		424	26-Oct-26	26-Dec-26	0	0	0	0	0%	0%
Issuance of Purchase Orders		88	26-Oct-26	07-Nov-26	0	0	0	0	0%	0%
Water Pump Station		32	26-Oct-26	29-Oct-26	0	0	0	0	0%	0%

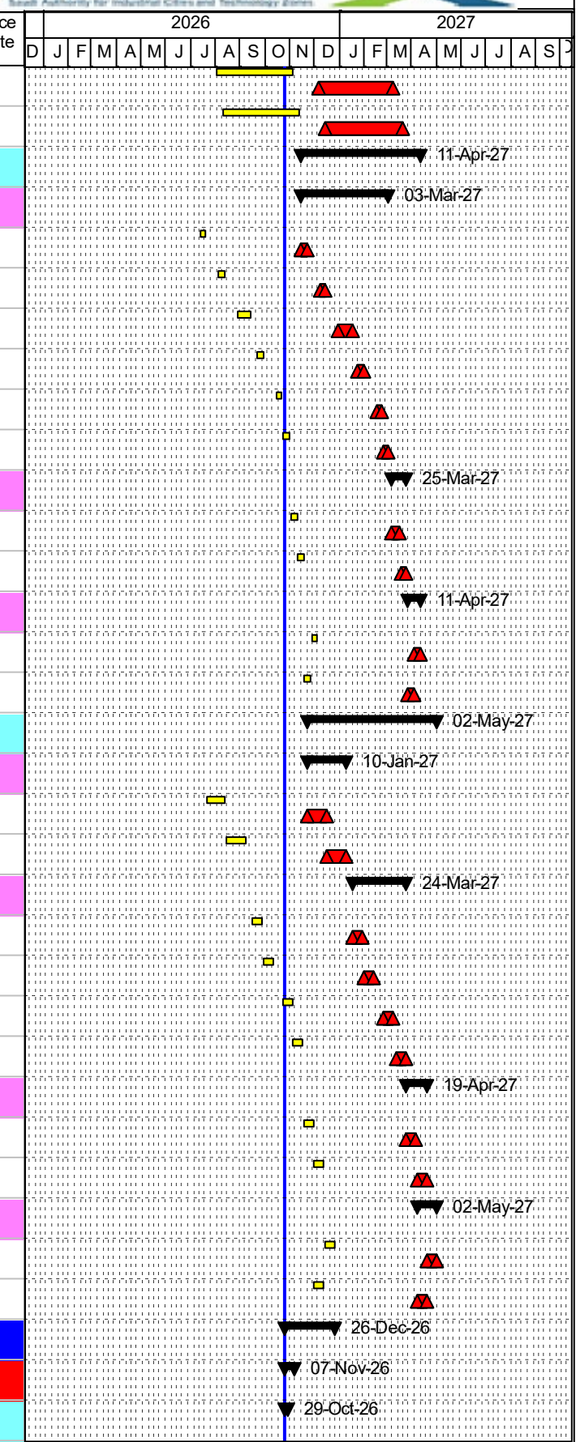


Primary Baseline | Actual Work | Summary
Remaining Work | Baseline Milestone
Critical Remaining Work | Milestone

Date	Revision	Checked	Approved
26-Oct-26	Third Industrial City		

Development of the Technology City in Dharan Project
BL-Update 26-10-2026
WPR UPS LEVEL 5


Activity ID	Activity Name	Original Duration	Start	Finish	Budgeted Total Cost	Planned Value Cost	Earned Value Cost	Actual Total Cost	Schedule % Complete	Performance % Complete
PRO-LS-CV-PO-20	Issuance of Purchase Order for Works for Water Pump Station	32	26-Oct-26	29-Oct-26	0	0	0	0	100%	0%
Storage Tank (TSE)		56	31-Oct-26	07-Nov-26	0	0	0	0	0%	0%
PRO-TSE-CV-PO-30	Issuance of Purchase Order for Works for Storage Tank (TSE)	56	31-Oct-26	07-Nov-26	0	0	0	0	100%	0%
Control Room		56	31-Oct-26	07-Nov-26	0	0	0	0	0%	0%
PRO-TSE-CV-PO-40	Issuance of Purchase Order for Works for Control Room	56	31-Oct-26	07-Nov-26	0	0	0	0	100%	0%
Sewage Pump Stations		56	31-Oct-26	07-Nov-26	0	0	0	0	0%	0%
PRO-SPS-CV-PO-10	Issuance of Purchase Order for Works of Sewage Pump Station	56	31-Oct-26	07-Nov-26	0	0	0	0	100%	0%
Gaurd Room		56	31-Oct-26	07-Nov-26	0	0	0	0	0%	0%
PRO-GR-CV-PO-40	Issuance of Purchase Order for Materials for Gaurd Room	56	31-Oct-26	07-Nov-26	0	0	0	0	100%	0%
Boundary Fence		56	31-Oct-26	07-Nov-26	0	0	0	0	0%	0%
PRO-FE-CV-PO-50	Issuance of Purchase Order for Materials for Boundary Fence	56	31-Oct-26	07-Nov-26	0	0	0	0	100%	0%
Manufacturing of Material		224	31-Oct-26	01-Dec-26	0	0	0	0	0%	0%
Water Pump Station		56	31-Oct-26	07-Nov-26	0	0	0	0	0%	0%
PRO-LS-CV-MF-30	Manufacturing of Works for Works for Water Pump Station	56	31-Oct-26	07-Nov-26	0	0	0	0	100%	0%
Storage Tank (TSE)		112	08-Nov-26	23-Nov-26	0	0	0	0	0%	0%
PRO-TSE-CV-MF-40	Manufacturing of Works for Storage Tank (TSE)	112	08-Nov-26	23-Nov-26	0	0	0	0	100%	0%
Control Room		168	08-Nov-26	01-Dec-26	0	0	0	0	0%	0%
PRO-TSE-CV-MF-50	Manufacturing of Works for Control Room	168	08-Nov-26	01-Dec-26	0	0	0	0	100%	0%
Sewage Pump Stations		168	08-Nov-26	01-Dec-26	0	0	0	0	0%	0%
PRO-SPS-CV-MF-10	Manufacturing of Works of Sewage Pump Station	168	08-Nov-26	01-Dec-26	0	0	0	0	100%	0%
Gaurd Room		168	08-Nov-26	01-Dec-26	0	0	0	0	0%	0%
PRO-GR-CV-MF-50	Manufacturing of Materials for Gaurd Room	168	08-Nov-26	01-Dec-26	0	0	0	0	100%	0%
Boundary Fence		168	08-Nov-26	01-Dec-26	0	0	0	0	0%	0%
PRO-FE-CV-MF-60	Manufacturing of Materials for Boundary Fence	168	08-Nov-26	01-Dec-26	0	0	0	0	100%	0%
1st Material Delivery & Site Inspection		280	31-Oct-26	09-Dec-26	0	0	0	0	0%	0%
Water Pump Station		48	31-Oct-26	05-Nov-26	0	0	0	0	0%	0%
PRO-LS-CV-1DL-40	1ST Material Delivery for Works of Water Pump Station	48	31-Oct-26	05-Nov-26	0	0	0	0	100%	0%
Storage Tank (TSE)		56	24-Nov-26	01-Dec-26	0	0	0	0	0%	0%
PRO-TSE-CV-1DL-50	1ST Material Delivery for Works for Storage Tank (TSE)	56	24-Nov-26	01-Dec-26	0	0	0	0	100%	0%
Control Room		56	02-Dec-26	09-Dec-26	0	0	0	0	0%	0%
PRO-TSE-CV-1DL-60	1ST Material Delivery for Works for Control Room	56	02-Dec-26	09-Dec-26	0	0	0	0	100%	0%
Sewage Pump Stations		56	02-Dec-26	09-Dec-26	0	0	0	0	0%	0%
PRO-SPS-CV-1DL-10	1ST Material Delivery for Works of Sewage Pump Station	56	02-Dec-26	09-Dec-26	0	0	0	0	100%	0%
Gaurd Room		56	02-Dec-26	09-Dec-26	0	0	0	0	0%	0%

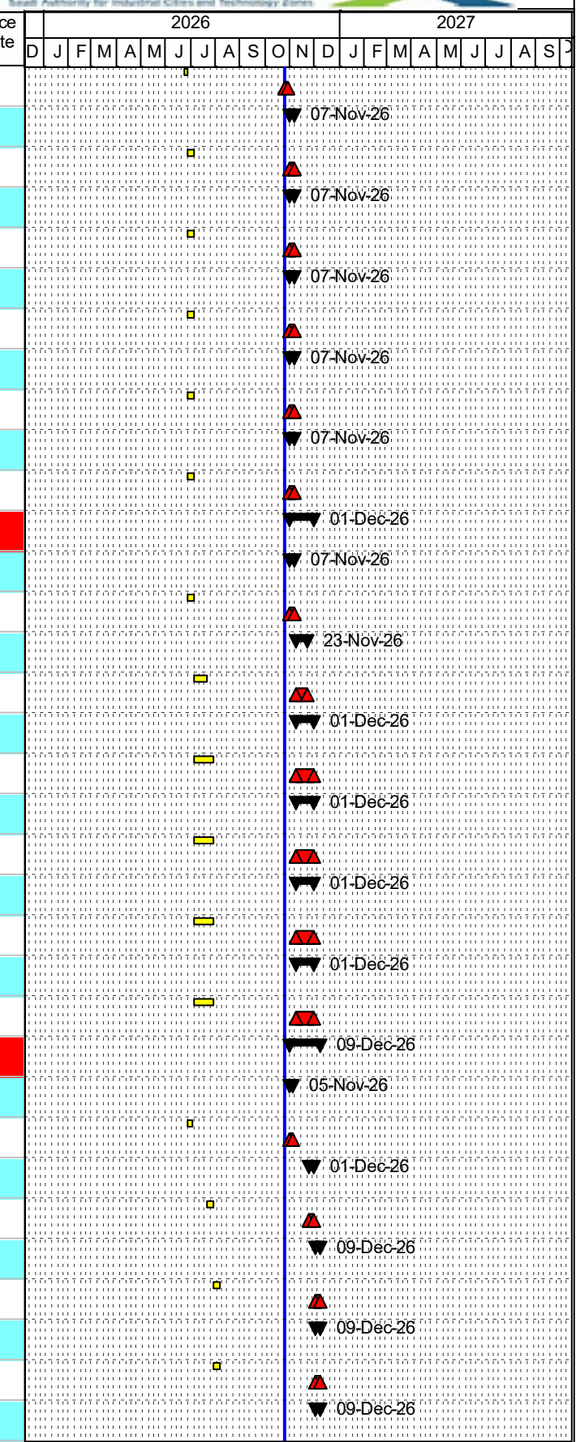

Primary Baseline | Actual Work | Summary
Remaining Work | Baseline Milestone
Critical Remaining Work | Milestone

Date	Revision	Checked	Approved
26-Oct-26	Third Industrial City		

Activity ID	Activity Name	Original Duration	Start	Finish	Budgeted Total Cost	Planned Value Cost	Earned Value Cost	Actual Total Cost	Schedule % Complete	Performance % Complete
PRO-GR-CV-1DL-60	1ST Material Delivery for Materials for Gaurd Room	56	02-Dec-26	09-Dec-26	0	0	0	0	100%	0%
Boundary Fence		56	02-Dec-26	09-Dec-26	0	0	0	0	0%	0%
PRO-FE-CV-1DL-70	1ST Material Delivery for Materials for Boundary Fence	56	02-Dec-26	09-Dec-26	0	0	0	0	100%	0%
Material Delivery & Site Inspection		392	31-Oct-26	26-Dec-26	0	0	0	0	0%	0%
Water Pump Station		80	31-Oct-26	10-Nov-26	0	0	0	0	0%	0%
PRO-LS-CV-DL-50	Material Delivery & Site Inspection for Works for Water Pump Station	80	31-Oct-26	10-Nov-26	0	0	0	0	100%	0%
Storage Tank (TSE)		216	11-Nov-26	12-Dec-26	0	0	0	0	0%	0%
PRO-TSE-CV-DL-60	Material Delivery & Site Inspection for Works for Storage Tank (TSE)	216	11-Nov-26	12-Dec-26	0	0	0	0	100%	0%
Control Room		112	10-Dec-26	26-Dec-26	0	0	0	0	0%	0%
PRO-TSE-CV-DL-70	Material Delivery & Site Inspection for Works for Control Room	112	10-Dec-26	26-Dec-26	0	0	0	0	100%	0%
Sewage Pump Stations		112	10-Dec-26	26-Dec-26	0	0	0	0	0%	0%
PRO-SPS-CV-DL-10	Material Delivery & Site Inspection for Works for Pump Station	112	10-Dec-26	26-Dec-26	0	0	0	0	100%	0%
Gaurd Room		112	10-Dec-26	26-Dec-26	0	0	0	0	0%	0%
PRO-GR-CV-DL-70	Material Delivery & Site Inspection for Materials for Gaurd Room	112	10-Dec-26	26-Dec-26	0	0	0	0	100%	0%
Boundary Fence		112	10-Dec-26	26-Dec-26	0	0	0	0	0%	0%
PRO-FE-CV-DL-80	Material Delivery & Site Inspection for Materials for Boundary Fence	112	10-Dec-26	26-Dec-26	0	0	0	0	100%	0%
Softscape and Planting Works		736	11-Nov-26	25-Feb-27	0	0	0	0	0%	0%
Issuance of Purchase Orders		96	11-Nov-26	24-Nov-26	0	0	0	0	0%	0%
Main Line Pipes		96	11-Nov-26	24-Nov-26	0	0	0	0	0%	0%
PRO-IR-PO-140	Issuance of Purchase Order for Softscape and Planting Works	48	11-Nov-26	17-Nov-26	0	0	0	0	100%	0%
PRO-IR-PO-150	Issuance of Purchase Order for Site Furnishings (Seating Bench,Stone Boulders	48	18-Nov-26	24-Nov-26	0	0	0	0	100%	0%
Manufacturing of Material		528	18-Nov-26	02-Feb-27	0	0	0	0	0%	0%
Main Line Pipes		528	18-Nov-26	02-Feb-27	0	0	0	0	0%	0%
PRO-IR-MF-140	Manufacturing of Softscape and Planting Works	480	18-Nov-26	26-Jan-27	0	0	0	0	100%	0%
PRO-IR-MF-150	Manufacturing of Valves for Site Furnishings (Seating Bench,Stone Boulders and Gravel)	480	25-Nov-26	02-Feb-27	0	0	0	0	100%	0%
1st Material Delivery & Site Inspection		96	27-Jan-27	09-Feb-27	0	0	0	0	0%	0%
Main Line Pipes		96	27-Jan-27	09-Feb-27	0	0	0	0	0%	0%
PRO-IR-1DL-140	1ST Material Delivery for Softscape and Planting Works	48	27-Jan-27	02-Feb-27	0	0	0	0	100%	0%
PRO-IR-1DL-150	1ST Material Delivery for Site Furnishings (Seating Bench,Stone Boulders and Gravel)	48	03-Feb-27	09-Feb-27	0	0	0	0	100%	0%
Material Delivery & Site Inspection		160	03-Feb-27	25-Feb-27	0	0	0	0	0%	0%
Main Line Pipes		160	03-Feb-27	25-Feb-27	0	0	0	0	0%	0%
PRO-R25-IR-DL-140	Material Delivery & Site Inspection of Softscape and Planting Works	80	03-Feb-27	14-Feb-27	0	0	0	0	100%	0%
PRO-R25-IR-DL-150	Material Delivery & Site Inspection of Site Furnishings (Seating Bench,Stone Boulders	80	15-Feb-27	25-Feb-27	0	0	0	0	100%	0%
Long Lead Time Items		1456	11-Nov-26	20-Jun-27	0	0	0	0	0%	0%

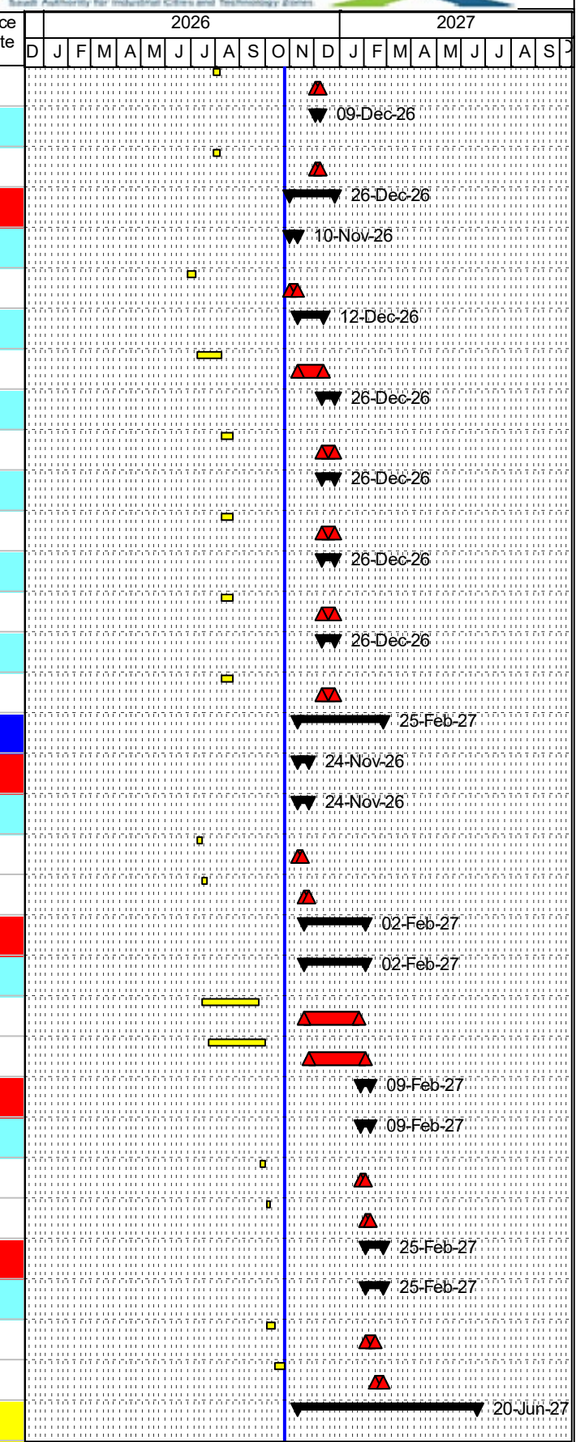


Primary Baseline | Actual Work | Summary
Remaining Work | Baseline Milestone
Critical Remaining Work | Milestone

Date	Revision	Checked	Approved
26-Oct-26	Third Industrial City		

Development of the Technology City in Dharan Project
BL-Update 26-10-2026
WPR UPS LEVEL 5

Activity ID	Activity Name	Original Duration	Start	Finish	Budgeted Total Cost	Planned Value Cost	Earned Value Cost	Actual Total Cost	Schedule % Complete	Performance % Complete
Superstructure Works		1456	11-Nov-26	20-Jun-27	0	0	0	0	0%	0%
Sewage Pump Station		1192	11-Nov-26	06-May-27	0	0	0	0	0%	0%
Issuance of Purchase Orders		48	11-Nov-26	17-Nov-26	0	0	0	0	0%	0%
PRO-SPS-LL-PO-10	Issuance of Purchase Order for Electromechanical Works for Pump Station	48	11-Nov-26	17-Nov-26	0	0	0	0	100%	0%
Manufacturing of Material		800	18-Nov-26	17-Mar-27	0	0	0	0	0%	0%
PRO-SPS-LL-MF-10	Manufacturing of Electromechanical Works for Pump Station	800	18-Nov-26	17-Mar-27	0	0	0	0	86%	0%
Material Shipping/Custom Clearance/Delivery		168	18-Mar-27	11-Apr-27	0	0	0	0	0%	0%
PRO-SPS-LL-SH/DL-10	Material Delivery for Electromechanical Works for Pump Station	168	18-Mar-27	11-Apr-27	0	0	0	0	0%	0%
Material Site Inspection		176	12-Apr-27	06-May-27	0	0	0	0	0%	0%
PRO-SPS-LL-MSI-10	Material Site Inspection for Electromechanical Works for Pump Station	176	12-Apr-27	06-May-27	0	0	0	0	0%	0%
Water Pump Station		952	18-Nov-26	08-Apr-27	0	0	0	0	0%	0%
Issuance of Purchase Orders		56	18-Nov-26	25-Nov-26	0	0	0	0	0%	0%
PRO-LS-LL-PO-20	Issuance of Purchase Order for Electromechanical Works for Water Pump	56	18-Nov-26	25-Nov-26	0	0	0	0	100%	0%
Manufacturing of Material		560	26-Nov-26	15-Feb-27	0	0	0	0	0%	0%
PRO-LS-LL-MF-20	Manufacturing of Electromechanical Works for Water Pump Station	560	26-Nov-26	15-Feb-27	0	0	0	0	100%	0%
Material Shipping/Custom Clearance/Delivery		168	16-Feb-27	15-Mar-27	0	0	0	0	0%	0%
PRO-LS-LL-SH/DL-20	Material Delivery for Electromechanical Works for Water Pump Station	168	16-Feb-27	15-Mar-27	0	0	0	0	42.86%	0%
Material Site Inspection		168	16-Mar-27	08-Apr-27	0	0	0	0	0%	0%
PRO-LS-LL-MSI-20	Material Site Inspection for Electromechanical Works for Water Pump Station	168	16-Mar-27	08-Apr-27	0	0	0	0	0%	0%
Storage Tank (TSE)		1352	26-Nov-26	20-Jun-27	0	0	0	0	0%	0%
Issuance of Purchase Orders		56	26-Nov-26	03-Dec-26	0	0	0	0	0%	0%
PRO-TSE-LL-PO-30	Issuance of Purchase Order for Electromechanical Works for Storage Tank	56	26-Nov-26	03-Dec-26	0	0	0	0	100%	0%
Manufacturing of Material		960	05-Dec-26	26-Apr-27	0	0	0	0	0%	0%
PRO-TSE-LL-MF-30	Manufacturing of Electromechanical Works for Storage Tank (TSE)	960	05-Dec-26	26-Apr-27	0	0	0	0	60%	0%
Material Shipping/Custom Clearance/Delivery		168	27-Apr-27	26-May-27	0	0	0	0	0%	0%
PRO-TSE-LL-SH/DL-30	Material Delivery for Electromechanical Works for Storage Tank (TSE)	168	27-Apr-27	26-May-27	0	0	0	0	0%	0%
Material Site Inspection		168	27-May-27	20-Jun-27	0	0	0	0	0%	0%
PRO-TSE-LL-MSI-30	Material Site Inspection for Electromechanical Works for Storage Tank (TSE)	168	27-May-27	20-Jun-27	0	0	0	0	0%	0%
Construction Works		3102	10-Mar-26 A	23-Jun-27	93,388,700	35,616,581	23,396,765	22,760,264	38.14%	25.05%
Infrastructure Networks		3086	10-Mar-26 A	21-Jun-27	57,696,530	32,596,024	13,726,670	13,448,654	56.5%	23.79%
Internal		3086	10-Mar-26 A	21-Jun-27	32,508,953	16,942,289	3,102,401	3,102,629	52.12%	9.54%
Alignment-RD-01		2950	10-Mar-26 A	01-Jun-27	15,199,337	8,358,281	3,102,401	3,102,629	54.99%	20.41%
Earthworks		1774	10-Mar-26 A	06-Jan-27	4,697,995	4,697,995	3,055,456	3,055,656	100%	65.04%
Earthworks		1774	10-Mar-26 A	06-Jan-27	4,697,995	4,697,995	3,055,456	3,055,656	100%	65.04%

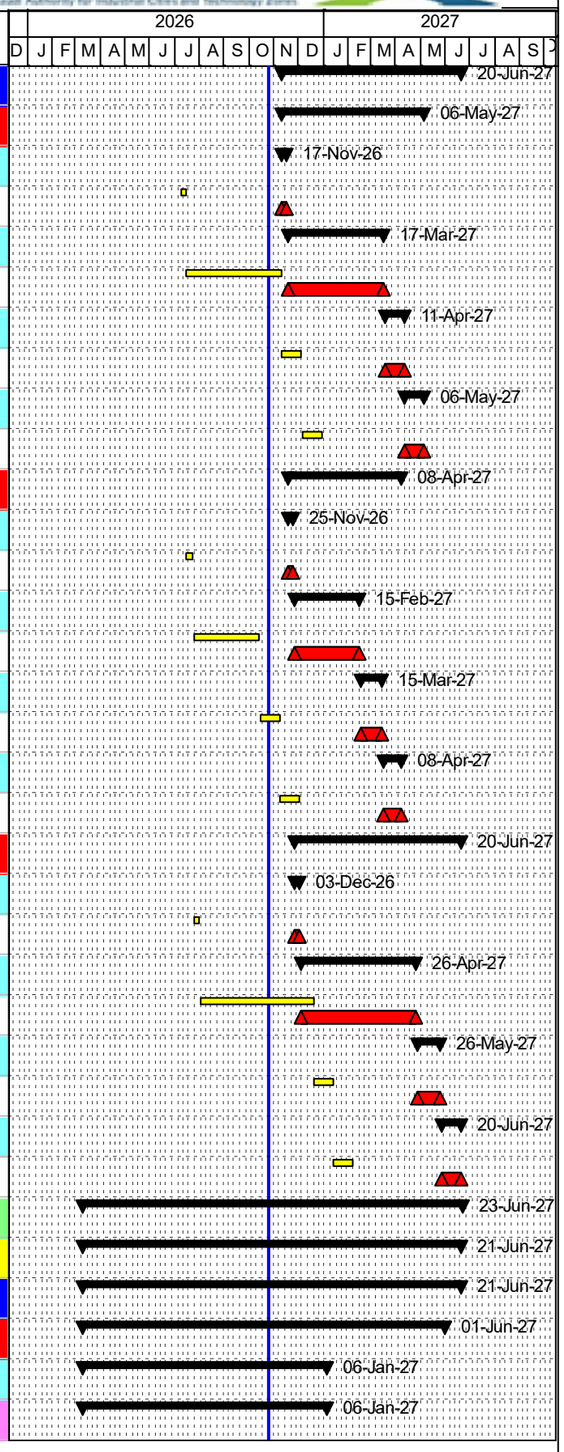


Primary Baseline | Actual Work | Summary
Remaining Work | Baseline Milestone
Critical Remaining Work | Milestone

Date	Revision	Checked	Approved
26-Oct-26	Third Industrial City		

Development of the Technology City in Dharan Project
BL-Update 26-10-2026
WPR UPS LEVEL 5


Activity ID	Activity Name	Original Duration	Start	Finish	Budgeted Total Cost	Planned Value Cost	Earned Value Cost	Actual Total Cost	Schedule % Complete	Performance % Complete
CO-EW-210	Excavation and Backfilling Works Upto Design Level for Earthworks for	648	10-Mar-26 A	22-Jun-26 A	379,596	379,596	379,596	379,596	100%	100%
CO-EW-210_R	Excavation and Backfilling Works Upto Design Level for Earthworks for	160	01-Jul-26 A	15-Jul-26 A	1,772,616	1,772,616	1,772,616	1,772,616	100%	100%
CO-EW-210_R01	Excavation and Backfilling Works Upto Design Level for Earthworks for	160	31-Aug-26 A	06-Jan-27	2,545,782	2,545,782	903,244	903,443	100%	35.48%
Storm Drainage Network		488	20-Oct-26 A	04-Jan-27	2,292,989	2,292,989	46,945	46,973	100%	2.05%
Manholes		328	26-Oct-26	12-Dec-26	340,545	340,545	0	0	100%	0%
CO-SD-MH-230	Trench Excavation and Bedding Works for Manholes of Storm Drainage Network for	96	26-Oct-26	08-Nov-26	22,703	22,703	0	0	100%	0%
CO-SD-MH-240	Install RC Footing Works for Manholes of Storm Drainage Network for Alignment-RD-01	72	12-Nov-26	22-Nov-26	113,515	113,515	0	0	100%	0%
CO-SD-MH-250	Install RC Wall Rings & Slab Works for Manholes of Storm Drainage Network for	56	23-Nov-26	30-Nov-26	136,218	136,218	0	0	100%	0%
CO-SD-MH-260	Backfilling Works for Manholes of Storm Drainage Network for Alignment-RD-01	80	01-Dec-26	12-Dec-26	68,109	68,109	0	0	100%	0%
Main Line Sections		184	20-Oct-26 A	19-Dec-26	1,523,566	1,523,566	46,945	46,973	100%	3.08%
CO-SD-ML-140	Trench Excavation and Bedding Works for Main Lines of Storm Drainage Network for	64	20-Oct-26 A	01-Dec-26	209,385	209,385	0	0	100%	0%
CO-SD-ML-150	Pipes Laying Works for Main Lines of Storm Drainage Network for Alignment-RD-01	64	20-Oct-26 A	09-Dec-26	933,291	933,291	46,945	46,973	100%	5.03%
CO-SD-ML-160	Trench Backfilling and Compaction Works for Main Lines of Storm Drainage Network for	64	20-Oct-26 A	19-Dec-26	380,890	380,890	0	0	100%	0%
Catch Basin Sections		176	10-Dec-26	04-Jan-27	428,877	428,877	0	0	100%	0%
CO-SD-CB-180	Trench Excavation and Bedding Works for Catch Basins of Storm Drainage Network for	64	10-Dec-26	19-Dec-26	107,219	107,219	0	0	100%	0%
CO-SD-CB-190	Installation and Pipes Laying Connection Works for Catch Basins of Storm Drainage	56	20-Dec-26	27-Dec-26	250,178	250,178	0	0	100%	0%
CO-SD-CB-200	Trench Backfilling and Compaction Works for Catch Basins of Storm Drainage Network for	56	28-Dec-26	04-Jan-27	71,479	71,479	0	0	100%	0%
Sewage Network		480	20-Dec-26	27-Feb-27	801,144	747,593	0	0	93.32%	0%
Manholes		480	20-Dec-26	27-Feb-27	264,213	255,406	0	0	96.67%	0%
CO-SW-MH-210	Excavation Works for Main Line Manholes of Sewage Network for Alignment-RD-01	96	20-Dec-26	02-Jan-27	17,614	17,614	0	0	100%	0%
CO-SW-MH-220	Installation RC Footing Works for Main Line Manholes of Sewage Network for	96	03-Jan-27	16-Jan-27	88,071	88,071	0	0	100%	0%
CO-SW-MH-230	Install Grp Liner Wall Works for Main Line Manholes of Sewage Network for	96	17-Jan-27	30-Jan-27	52,843	52,843	0	0	100%	0%
CO-SW-MH-240	Pouring Grp Liner Wall Works for Main Line Manholes of Sewage Network for	96	31-Jan-27	13-Feb-27	52,843	52,843	0	0	100%	0%
CO-SW-MH-250	Backfilling Works for Main Line Manholes of Sewage Network for Alignment-RD-01	96	14-Feb-27	27-Feb-27	52,843	44,036	0	0	83.33%	0%
Main Line Sections		368	05-Jan-27	27-Feb-27	536,930	492,187	0	0	91.67%	0%
CO-SW-ML-140	Trench Excavation and Bedding Works for Main Lines of Sewage Network for	64	05-Jan-27	13-Jan-27	79,139	79,139	0	0	100%	0%
CO-SW-ML-150	Pipes Laying Works for Main Lines of Sewage Network for Alignment-RD-01	64	14-Jan-27	23-Jan-27	323,562	323,562	0	0	100%	0%
CO-SW-ML-160	Trench Backfilling and Compaction Works for Main Lines of Sewage Network for	48	21-Feb-27	27-Feb-27	134,230	89,487	0	0	66.67%	0%
Treated Sewage Effluent (Tse)		336	13-Dec-26	30-Jan-27	94,795	94,795	0	0	100%	0%
CO-TSE-ML-200	Trench Excavation and Bedding Works for Main Lines of Treated Sewage Effluent (Tse)	56	13-Dec-26	20-Dec-26	11,940	11,940	0	0	100%	0%
CO-TSE-ML-210	Pipes Laying Works for Main Lines of Treated Sewage Effluent (Tse) for Alignment-RD-01	136	26-Dec-26	13-Jan-27	59,156	59,156	0	0	100%	0%
CO-TSE-ML-230	Trench Backfilling and Compaction Works for Treated Sewage Effluent (Tse) for	112	14-Jan-27	30-Jan-27	23,699	23,699	0	0	100%	0%
Potable Water Network		256	13-Dec-26	18-Jan-27	373,599	373,599	0	0	100%	0%
Main Line Sections		256	13-Dec-26	18-Jan-27	248,155	248,155	0	0	100%	0%

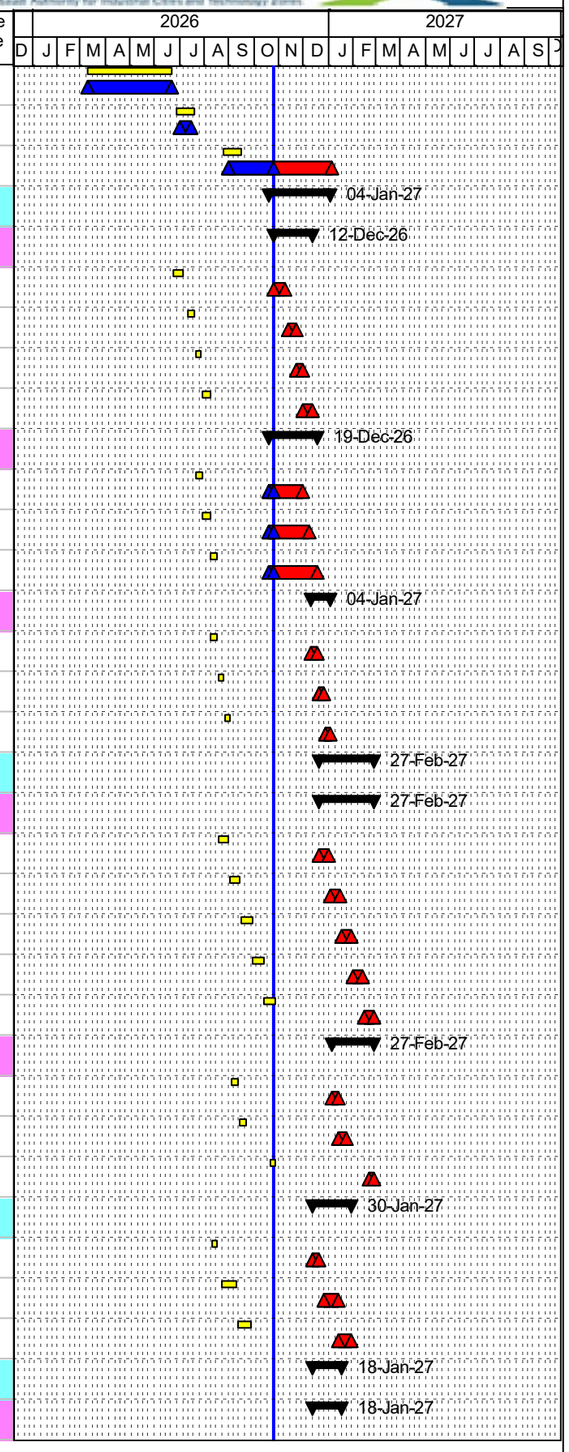

Primary Baseline | Actual Work | Summary
Remaining Work | Baseline Milestone
Critical Remaining Work | Milestone

Date	Revision	Checked	Approved
26-Oct-26	Third Industrial City		


Activity ID	Activity Name	Original Duration	Start	Finish	Budgeted Total Cost	Planned Value Cost	Earned Value Cost	Actual Total Cost	Schedule % Complete	Performance % Complete
CO-PW-ML-140	Trench Excavation and Bedding Works for Main Lines of Potable Water Network for	48	13-Dec-26	19-Dec-26	45,473	45,473	0	0	100%	0%
CO-PW-ML-150	Pipes Laying and accessories for Main Lines of Potable Water Network for	48	05-Jan-27	11-Jan-27	112,515	112,515	0	0	100%	0%
CO-PW-ML-160	Trench Backfilling and Compaction Works for Main Lines of Potable Water Network for	48	12-Jan-27	18-Jan-27	90,167	90,167	0	0	100%	0%
Valve Chamber		240	15-Dec-26	18-Jan-27	62,485	62,485	0	0	100%	0%
CO-PW-VC-230	Excavation Works for Main Line Valves and Valve Chambers of Potable Water Network for	32	15-Dec-26	19-Dec-26	3,905	3,905	0	0	100%	0%
CO-PW-VC-240	Installation Works for Valves of Potable Water Network for Alignment-RD-01	32	24-Dec-26	28-Dec-26	10,154	10,154	0	0	100%	0%
CO-PW-VC-250	Backfilling Works for Main Line Valves and Valve Chambers of Potable Water Network for	32	14-Jan-27	18-Jan-27	7,811	7,811	0	0	100%	0%
CO-PW-VC190	Installation of Valve Chambers of Potable Water Network for Alignment-RD-01	32	20-Dec-26	23-Dec-26	40,615	40,615	0	0	100%	0%
Fire Hydrant		208	20-Dec-26	18-Jan-27	62,959	62,959	0	0	100%	0%
CO-PW-FH-170	Excavation Works for Fire Hydrants of Potable Water Network for Alignment-RD-01	120	20-Dec-26	05-Jan-27	3,935	3,935	0	0	100%	0%
CO-PW-FH-180	Installation Works for Fire Hydrant of Potable Water Network for Alignment-RD-01	24	12-Jan-27	14-Jan-27	51,154	51,154	0	0	100%	0%
CO-PW-FH-190	Trench Backfilling and Compaction Works for Fire Hydrants of Potable Water Network for	24	16-Jan-27	18-Jan-27	7,870	7,870	0	0	100%	0%
Irrigation Network		288	31-Jan-27	16-Mar-27	601,521	151,310	0	0	25.15%	0%
Main Line Pipes		288	31-Jan-27	16-Mar-27	601,521	151,310	0	0	25.15%	0%
CO-IR-ML-150	Trench Excavation and Bedding Works for Main Lines of Irrigation Network for	56	31-Jan-27	07-Feb-27	13,844	13,844	0	0	100%	0%
CO-IR-ML-160	Pipes Laying Works for Main Lines of Irrigation Network for Alignment-RD-01	64	08-Feb-27	16-Feb-27	69,218	69,218	0	0	100%	0%
CO-IR-ML-170	Installation Works for Main Line Valves of Irrigation Network for Alignment-RD-01	56	17-Feb-27	24-Feb-27	21,302	21,302	0	0	100%	0%
CO-IR-ML-180	Trench Backfilling and Compaction Works for Main Lines of Irrigation Network for	32	13-Mar-27	16-Mar-27	27,687	0	0	0	0%	0%
CO-IR-ML-190	Installation Works for Bulbblers And Sprinklers and Irrigation Control System of Irrigation	80	25-Feb-27	08-Mar-27	469,471	46,947	0	0	10%	0%
Medium Voltage Network		144	28-Feb-27	23-Mar-27	153,221	0	0	0	0%	0%
Cabling Works		144	28-Feb-27	23-Mar-27	153,221	0	0	0	0%	0%
CO-MV-ML-280	Trench Excavation and Bedding Works for Medium Voltage Network for Alignment-RD-01	48	28-Feb-27	06-Mar-27	29,351	0	0	0	0%	0%
CO-MV-ML-290	Duct Laying Works for Medium Voltage Network for Alignment-RD-01	48	07-Mar-27	16-Mar-27	85,162	0	0	0	0%	0%
CO-MV-ML-300	Trench Backfilling and Compaction Works for Medium Voltage Network for Alignment-RD-01	48	17-Mar-27	23-Mar-27	38,709	0	0	0	0%	0%
Low Voltage Network		200	24-Mar-27	21-Apr-27	158,103	0	0	0	0%	0%
Main Low Voltage Cables Works (Cable 300 MM)		144	24-Mar-27	13-Apr-27	81,711	0	0	0	0%	0%
CON-LV-ML-130	Trench Excavation and Bedding Works for Main Cable of Low Voltage Network for	48	24-Mar-27	30-Mar-27	15,956	0	0	0	0%	0%
CON-LV-ML-140	Cable Laying Works for Main Cable of Low Voltage Network for Alignment-RD-01	48	31-Mar-27	06-Apr-27	45,209	0	0	0	0%	0%
CON-LV-ML-150	Trench Backfilling and Compaction Works for Main Cable of Low Voltage Network for	48	07-Apr-27	13-Apr-27	20,546	0	0	0	0%	0%
Service Low Voltage Cables Works (Cable 70 MM)		152	31-Mar-27	21-Apr-27	73,733	0	0	0	0%	0%
CON-LV-HC-130	Trench Excavation and Bedding Works for Service Cable of Low Voltage Network for	48	31-Mar-27	06-Apr-27	7,978	0	0	0	0%	0%
CON-LV-HC-140	Cable Laying Works for Service Cable of Low Voltage Network for Alignment-RD-01	56	07-Apr-27	14-Apr-27	45,209	0	0	0	0%	0%
CON-LV-HC-150	Trench Backfilling and Compaction Works for Service Cable of Low Voltage Network for	48	15-Apr-27	21-Apr-27	20,546	0	0	0	0%	0%
Distribution Pillars Works		56	31-Mar-27	07-Apr-27	2,659	0	0	0	0%	0%

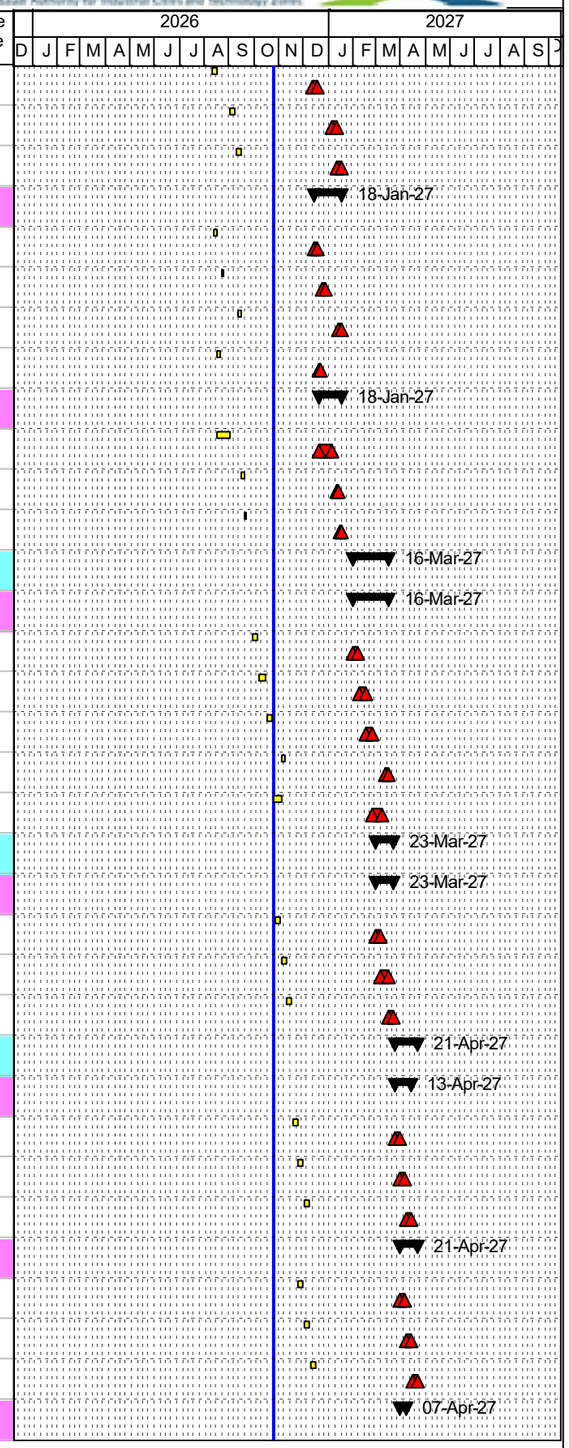

Primary Baseline | Actual Work | Summary
Remaining Work | Baseline Milestone
Critical Remaining Work | Milestone

Date	Revision	Checked	Approved
26-Oct-26	Third Industrial City		


Activity ID	Activity Name	Original Duration	Start	Finish	Budgeted Total Cost	Planned Value Cost	Earned Value Cost	Actual Total Cost	Schedule % Complete	Performance % Complete
CON-LV-DP-130	Foundation Excavation Works for Distribution Pillars of Low Voltage Network for	56	31-Mar-27	07-Apr-27	2,659	0	0	0	0%	0%
Street Lighting Network		184	07-Mar-27	05-Apr-27	80,615	0	0	0	0%	0%
Lighting Poles Works		152	07-Mar-27	31-Mar-27	33,194	0	0	0	0%	0%
CO-SL-LP-350	Installation Works for Lighting Poles Foundation of Street Lighting Network for	64	07-Mar-27	18-Mar-27	7,113	0	0	0	0%	0%
CO-SL-LP-360	Installation Works for Lighting Poles of Street Lighting Network for Alignment-RD-01	40	20-Mar-27	24-Mar-27	23,710	0	0	0	0%	0%
CO-SL-LP-380	Backfilling Works for Lighting Poles of Street Lighting Network for Alignment-RD-01	48	25-Mar-27	31-Mar-27	2,371	0	0	0	0%	0%
Cabling Works		80	25-Mar-27	05-Apr-27	47,420	0	0	0	0%	0%
CO-SL-CL-290	Cable Laying Works for Street Lighting Network for Alignment-RD-01	40	25-Mar-27	30-Mar-27	26,081	0	0	0	0%	0%
CO-SL-CL-300	Trench Backfilling and Compaction Works for Street Lighting Network for Alignment-RD-01	40	31-Mar-27	05-Apr-27	21,339	0	0	0	0%	0%
Telecom and Light Current Network		168	06-Apr-27	29-Apr-27	1,517,343	0	0	0	0%	0%
Ducts Works		56	22-Apr-27	29-Apr-27	94,908	0	0	0	0%	0%
CO-TE-DW-150	Pipes Laying Works for Ducts of Telecom Network for Alignment-RD-01	32	22-Apr-27	26-Apr-27	65,249	0	0	0	0%	0%
CO-TE-DW-160	Trench Backfilling and Compaction Works for Ducts of Telecom Network for	24	27-Apr-27	29-Apr-27	29,659	0	0	0	0%	0%
Manholes Works		64	06-Apr-27	14-Apr-27	36,239	0	0	0	0%	0%
CO-TE-MH-170	Excavation Works for Manholes of Telecom Network for Alignment-RD-01	32	06-Apr-27	10-Apr-27	2,416	0	0	0	0%	0%
CO-TE-MH-180	Installation Works for Manholes of Telecom Network for Alignment-RD-01	32	06-Apr-27	10-Apr-27	26,575	0	0	0	0%	0%
CO-TE-MH-190	Backfilling Works for Manholes of Telecom Network for Alignment-RD-01	32	11-Apr-27	14-Apr-27	7,248	0	0	0	0%	0%
CCTV, Telephone, MSN, ACs System Works		64	15-Apr-27	24-Apr-27	1,386,196	0	0	0	0%	0%
CO-TE-CTV-150	Installation of CCTV, Telephone, ACS and MSN Systems Cables for Alignment-RD-01	64	15-Apr-27	24-Apr-27	1,386,196	0	0	0	0%	0%
Road Network		80	01-May-27	11-May-27	2,662,858	0	0	0	0%	0%
Pavement Works		80	01-May-27	11-May-27	2,607,263	0	0	0	0%	0%
CO-RD-PV-180	Fixing of Curbstone for Sidewalks Pavement for Alignment-RD-01	80	01-May-27	11-May-27	263,715	0	0	0	0%	0%
CO-RD-PV-190	Fixing of Interlock Tiles for Sidewalks Pavement for Alignment-RD-01	80	01-May-27	11-May-27	2,343,548	0	0	0	0%	0%
Traffic Signs Boards and Roads Marking		64	01-May-27	09-May-27	55,595	0	0	0	0%	0%
CO-RD-F-RM-190	Application of Road Marking Works For Road Works for Alignment-RD-01	32	01-May-27	04-May-27	35,713	0	0	0	0%	0%
CO-RD-F-TS-130	Installation Works of Traffic Signs Boards For Road Works for Alignment-RD-01	32	05-May-27	09-May-27	19,882	0	0	0	0%	0%
Finishes for Infrastructure Networks		440	24-Mar-27	01-Jun-27	1,765,154	0	0	0	0%	0%
Storm Drainage Network		184	01-May-27	01-Jun-27	780,323	0	0	0	0%	0%
Testing and Finishes		184	01-May-27	01-Jun-27	780,323	0	0	0	0%	0%
CO-SD-CB-TF-170	Testing Works for Catch Basins of Storm Drainage Network for Alignment-RD-01	56	12-May-27	25-May-27	71,479	0	0	0	0%	0%
CO-SD-CB-TF-180	Install Catch Basin Cover Works for External Finishes of Storm Drainage Network for	48	26-May-27	01-Jun-27	107,219	0	0	0	0%	0%
CO-SD-CB-TF-190	Catch Basin Internal Finishes (Benching) for Storm Drainage Network for Alignment-RD-01	48	01-May-27	06-May-27	107,219	0	0	0	0%	0%
CO-SD-MH-TF-230	Testing Works for Manholes of Storm Drainage Network for Alignment-RD-01	16	10-May-27	11-May-27	113,515	0	0	0	0%	0%
CO-SD-ML-TF-110	Testing Work for Pipes of Storm Drainage Network for Alignment-RD-01	16	08-May-27	09-May-27	380,890	0	0	0	0%	0%

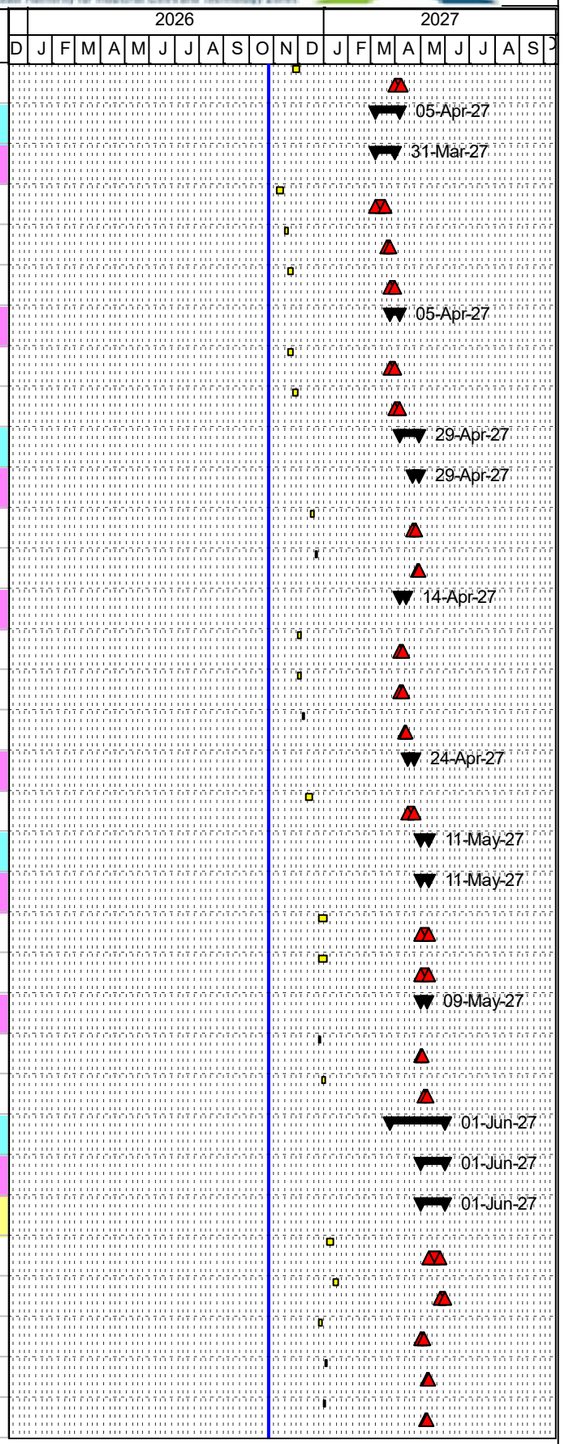

Primary Baseline | Actual Work | Summary
Remaining Work | Baseline Milestone
Critical Remaining Work | Milestone

Date	Revision	Checked	Approved
26-Oct-26	Third Industrial City		


Activity ID	Activity Name	Original Duration	Start	Finish	Budgeted Total Cost	Planned Value Cost	Earned Value Cost	Actual Total Cost	Schedule % Complete	Performance % Complete
Sewage Network		56	01-May-27	08-May-27	222,301	0	0	0	0%	0%
Testing and Finishes		56	01-May-27	08-May-27	222,301	0	0	0	0%	0%
CO-SW-TF-230	Final Testing For Main Line of Sewage Network for Alignment-RD-01	32	04-May-27	08-May-27	134,230	0	0	0	0%	0%
CO-SW-TF-250	Testing Works for Main Line Manholes of Sewage Network for Alignment-RD-01	24	01-May-27	03-May-27	88,071	0	0	0	0%	0%
Potable Water Network		64	01-May-27	09-May-27	234,043	0	0	0	0%	0%
Testing and Finishes		64	01-May-27	09-May-27	234,043	0	0	0	0%	0%
CO-PW-TF-140	Fire Hydrant Finishies (S.Box + Safety + Marker Post) of Potable Water Network for	32	01-May-27	04-May-27	15,740	0	0	0	0%	0%
CO-PW-TF-150	Final Finishes works and Covers for Valves and Valve Chambers for Alignment-RD-01	16	05-May-27	06-May-27	128,136	0	0	0	0%	0%
CO-PW-TF-220	Testing of Potable Water Network for Alignment-RD-01	16	08-May-27	09-May-27	90,167	0	0	0	0%	0%
Irrigation Network		16	10-May-27	11-May-27	27,687	0	0	0	0%	0%
Testing and Finishes		16	10-May-27	11-May-27	27,687	0	0	0	0%	0%
CO-IR-TF-170	Final Testing (pressure tests) of Irrigation Network for Alignment-RD-01	16	10-May-27	11-May-27	27,687	0	0	0	0%	0%
Treated Sewage Effluent (Tse)		16	10-May-27	11-May-27	23,699	0	0	0	0%	0%
Testing and Finishes		16	10-May-27	11-May-27	23,699	0	0	0	0%	0%
CO-TSE-TF-210	Final Testing (pressure tests) of Treated Sewage Effluent (Tse) for Alignment-RD-01	16	10-May-27	11-May-27	23,699	0	0	0	0%	0%
Medium Voltage Network		16	24-Mar-27	25-Mar-27	30,971	0	0	0	0%	0%
Termination and Testing Works		16	24-Mar-27	25-Mar-27	30,971	0	0	0	0%	0%
CO-MV-TF-230	Testing and Termination Works of Medium Voltage Network for Alignment-RD-01	16	24-Mar-27	25-Mar-27	30,971	0	0	0	0%	0%
Low Voltage Network		32	22-Apr-27	26-Apr-27	32,877	0	0	0	0%	0%
Termination and Testing Works		32	22-Apr-27	26-Apr-27	32,877	0	0	0	0%	0%
CON-LV-TT-120	Testing and Termination Works for Substation Low Voltage Panel Boards of Low Voltage	32	22-Apr-27	26-Apr-27	32,877	0	0	0	0%	0%
Street Lighting Network		184	06-Apr-27	02-May-27	30,897	0	0	0	0%	0%
Termination and Testing Works		184	06-Apr-27	02-May-27	27,118	0	0	0	0%	0%
CO-SL-LP-370	Installation Works for Lighting Fixtures With Drop Wire of Street Lighting Network for	48	06-Apr-27	12-Apr-27	12,892	0	0	0	0%	0%
CO-SL-TF-410	Testing Works for Lighting Poles of Street Lighting Network for Alignment-RD-01	24	29-Apr-27	02-May-27	14,226	0	0	0	0%	0%
Earthing System Works		40	24-Apr-27	28-Apr-27	3,779	0	0	0	0%	0%
CO-SL-ES-240	Install Earthing System Works for Lighting Poles of Street Lighting Network for	24	24-Apr-27	26-Apr-27	1,890	0	0	0	0%	0%
CO-SL-ES-250	Install Earthing System Works for Lighting Panel Boards of Street Lighting Network for	16	27-Apr-27	28-Apr-27	1,890	0	0	0	0%	0%
Telecom and Light Current Network		48	01-May-27	06-May-27	382,356	0	0	0	0%	0%
Testing and Finishes		48	01-May-27	06-May-27	382,356	0	0	0	0%	0%
CO-TE-CTV-TF-180	Testing and Interface modules with Telecom for Alignment-RD-01	24	01-May-27	03-May-27	35,807	0	0	0	0%	0%
CO-TE-CTV-TF-310	Testing and Interface modules with CCTV, Telephone, MSN and Access Control for	24	04-May-27	06-May-27	346,549	0	0	0	0%	0%
Alignment-RD-02		1392	22-Nov-26	21-Jun-27	7,655,882	3,978,072	0	0	51.96%	0%
Earthworks		96	22-Nov-26	05-Dec-26	2,314,449	2,314,449	0	0	100%	0%

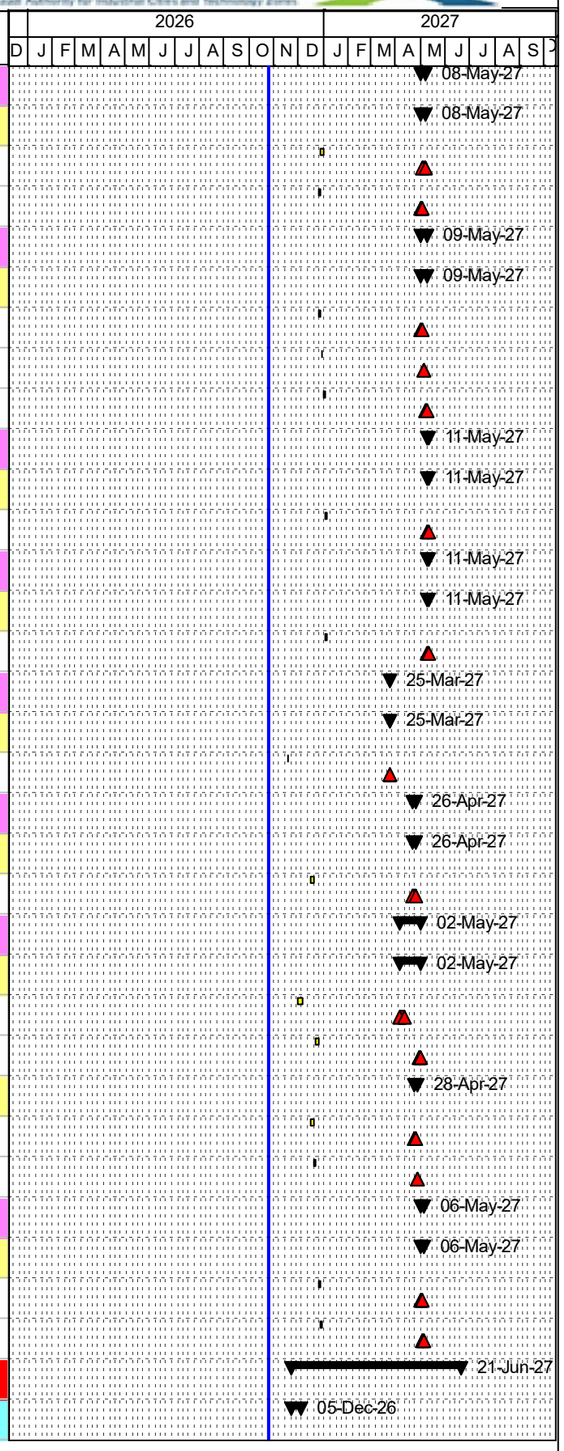

Primary Baseline | Actual Work | Summary
Remaining Work | Baseline Milestone
Critical Remaining Work | Milestone

Date	Revision	Checked	Approved
26-Oct-26	Third Industrial City		


Activity ID	Activity Name	Original Duration	Start	Finish	Budgeted Total Cost	Planned Value Cost	Earned Value Cost	Actual Total Cost	Schedule % Complete	Performance % Complete
Earthworks		96	22-Nov-26	05-Dec-26	2,314,449	2,314,449	0	0	100%	0%
CO-EW-220	Excavation and Backfilling Works Upto Design Level for Earthworks for Alignment-RD-02	96	22-Nov-26	05-Dec-26	2,314,449	2,314,449	0	0	100%	0%
Storm Drainage Network		744	06-Dec-26	27-Mar-27	1,062,822	1,028,976	0	0	96.82%	0%
Manholes		104	06-Dec-26	20-Dec-26	114,795	114,795	0	0	100%	0%
CO-SD-MH-270	Trench Excavation and Bedding Works for Manholes of Storm Drainage Network for	32	06-Dec-26	09-Dec-26	7,653	7,653	0	0	100%	0%
CO-SD-MH-280	Install RC Footing Works for Manholes of Storm Drainage Network for Alignment-RD-02	24	10-Dec-26	13-Dec-26	38,265	38,265	0	0	100%	0%
CO-SD-MH-290	Install RC Wall Rings & Slab Works for Manholes of Storm Drainage Network for	24	14-Dec-26	16-Dec-26	45,918	45,918	0	0	100%	0%
CO-SD-MH-300	Backfilling Works for Manholes of Storm Drainage Network for Alignment-RD-02	24	17-Dec-26	20-Dec-26	22,959	22,959	0	0	100%	0%
Main Line Sections		72	17-Dec-26	27-Dec-26	744,950	744,950	0	0	100%	0%
CO-SD-ML-170	Trench Excavation and Bedding Works for Main Lines of Storm Drainage Network for	24	17-Dec-26	20-Dec-26	106,954	106,954	0	0	100%	0%
CO-SD-ML-180	Pipes Laying Works for Main Lines of Storm Drainage Network for Alignment-RD-02	24	21-Dec-26	23-Dec-26	451,755	451,755	0	0	100%	0%
CO-SD-ML-190	Trench Backfilling and Compaction Works for Main Lines of Storm Drainage Network for	24	24-Dec-26	27-Dec-26	186,241	186,241	0	0	100%	0%
Catch Basin Sections		592	28-Dec-26	27-Mar-27	203,078	169,231	0	0	83.33%	0%
CO-SD-CB-210	Trench Excavation and Bedding Works for Catch Basins of Storm Drainage Network for	144	28-Dec-26	17-Jan-27	50,769	50,769	0	0	100%	0%
CO-SD-CB-220	Installation and Pipes Laying Connection Works for Catch Basins of Storm Drainage	152	18-Jan-27	08-Feb-27	118,462	118,462	0	0	100%	0%
CO-SD-CB-230	Trench Backfilling and Compaction Works for Catch Basins of Storm Drainage Network for	40	22-Mar-27	27-Mar-27	33,846	0	0	0	0%	0%
Sewage Network		464	28-Dec-26	04-Mar-27	276,597	225,194	0	0	81.42%	0%
Manholes		464	28-Dec-26	04-Mar-27	94,811	80,589	0	0	85%	0%
CO-SW-MH-260	Excavation Works for Main Line Manholes of Sewage Network for Alignment-RD-02	88	28-Dec-26	09-Jan-27	6,321	6,321	0	0	100%	0%
CO-SW-MH-270	Installation RC Footing Works for Main Line Manholes of Sewage Network for	88	10-Jan-27	21-Jan-27	31,604	31,604	0	0	100%	0%
CO-SW-MH-280	Install Grp Liner Wall Works for Main Line Manholes of Sewage Network for	96	23-Jan-27	04-Feb-27	18,962	18,962	0	0	100%	0%
CO-SW-MH-290	Pouring Grp Liner Wall Works for Main Line Manholes of Sewage Network for	96	06-Feb-27	18-Feb-27	18,962	18,962	0	0	100%	0%
CO-SW-MH-300	Backfilling Works for Main Line Manholes of Sewage Network for Alignment-RD-02	96	20-Feb-27	04-Mar-27	18,962	4,741	0	0	25%	0%
Main Line Sections		464	28-Dec-26	04-Mar-27	181,786	144,605	0	0	79.55%	0%
CO-SW-ML-170	Trench Excavation and Bedding Works for Main Lines of Sewage Network for	88	28-Dec-26	09-Jan-27	28,571	28,571	0	0	100%	0%
CO-SW-ML-180	Pipes Laying Works for Main Lines of Sewage Network for Alignment-RD-02	88	10-Jan-27	21-Jan-27	107,771	107,771	0	0	100%	0%
CO-SW-ML-190	Trench Backfilling and Compaction Works for Main Lines of Sewage Network for	88	21-Feb-27	04-Mar-27	45,443	8,262	0	0	18.18%	0%
Treated Sewage Effluent (Tse)		328	28-Dec-26	13-Feb-27	310,747	310,747	0	0	100%	0%
CO-TSE-ML-250	Trench Excavation and Bedding Works for Main Lines of Treated Sewage Effluent (Tse)	96	28-Dec-26	10-Jan-27	38,990	38,990	0	0	100%	0%
CO-TSE-ML-260	Pipes Laying Works for Main Lines of Treated Sewage Effluent (Tse) for Alignment-RD-02	136	11-Jan-27	30-Jan-27	194,070	194,070	0	0	100%	0%
CO-TSE-ML-280	Trench Backfilling and Compaction Works for Treated Sewage Effluent (Tse) for	96	31-Jan-27	13-Feb-27	77,686	77,686	0	0	100%	0%
Potable Water Network		144	14-Feb-27	06-Mar-27	232,618	98,705	0	0	42.43%	0%
Main Line Sections		136	14-Feb-27	04-Mar-27	77,824	29,338	0	0	37.7%	0%
CO-PW-ML-170	Trench Excavation and Bedding Works for Main Lines of Potable Water Network for	40	14-Feb-27	18-Feb-27	14,191	14,191	0	0	100%	0%

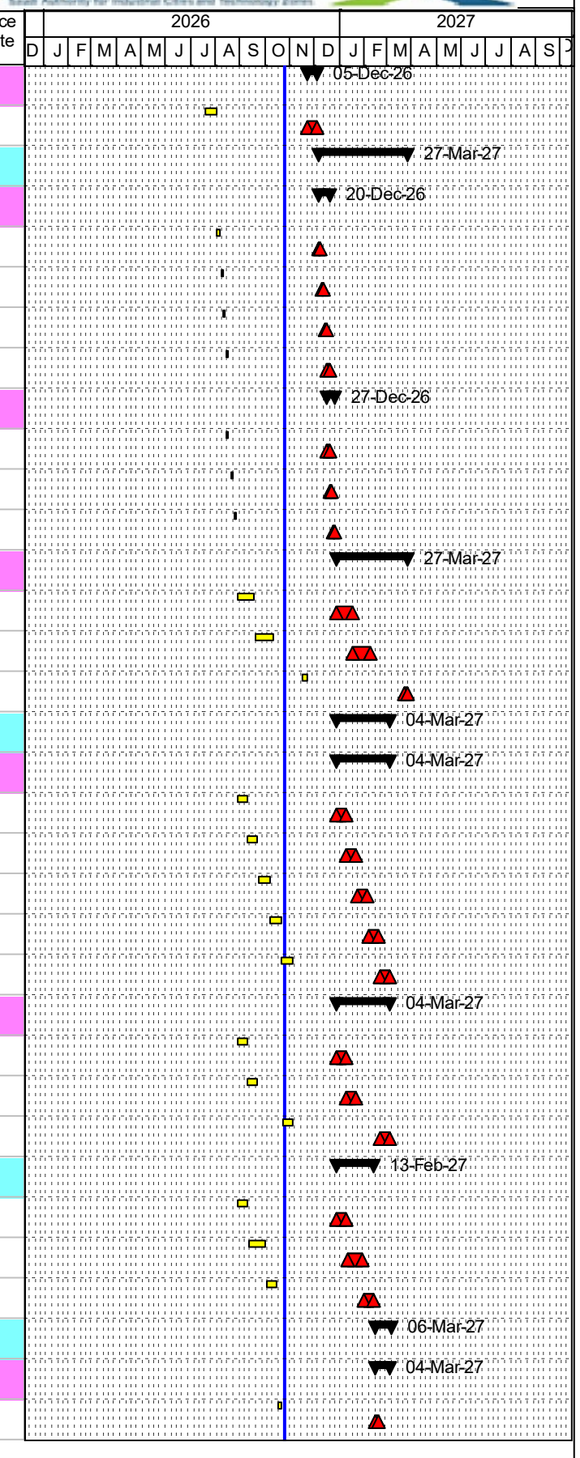

Primary Baseline
Actual Work
Summary
Remaining Work
Baseline Milestone
Critical Remaining Work
Milestone

Date	Revision	Checked	Approved
26-Oct-26	Third Industrial City		


Activity ID	Activity Name	Original Duration	Start	Finish	Budgeted Total Cost	Planned Value Cost	Earned Value Cost	Actual Total Cost	Schedule % Complete	Performance % Complete
CO-PW-ML-180	Pipes Laying and accessories for Main Lines of Potable Water Network for	56	20-Feb-27	27-Feb-27	35,342	15,147	0	0	42.86%	0%
CO-PW-ML-190	Trench Backfilling and Compaction Works for Main Lines of Potable Water Network for	40	28-Feb-27	04-Mar-27	28,291	0	0	0	0%	0%
Valve Chamber		144	14-Feb-27	06-Mar-27	91,835	65,432	0	0	71.25%	0%
CO-PW-VC-260	Excavation Works for Main Line Valves and Valve Chambers of Potable Water Network for	40	14-Feb-27	18-Feb-27	5,740	5,740	0	0	100%	0%
CO-PW-VC-270	Installation Works for Valves of Potable Water Network for Alignment-RD-02	40	23-Feb-27	28-Feb-27	14,923	0	0	0	0%	0%
CO-PW-VC-280	Backfilling Works for Main Line Valves and Valve Chambers of Potable Water Network for	40	01-Mar-27	06-Mar-27	11,479	0	0	0	0%	0%
CO-PW-VC200	Installation of Valve Chambers of Potable Water Network for Alignment-RD-02	24	20-Feb-27	22-Feb-27	59,693	59,693	0	0	100%	0%
Fire Hydrant		104	20-Feb-27	06-Mar-27	62,959	3,935	0	0	6.25%	0%
CO-PW-FH-200	Excavation Works for Fire Hydrants of Potable Water Network for Alignment-RD-02	24	20-Feb-27	22-Feb-27	3,935	3,935	0	0	100%	0%
CO-PW-FH-210	Installation Works for Fire Hydrant of Potable Water Network for Alignment-RD-02	24	28-Feb-27	02-Mar-27	51,154	0	0	0	0%	0%
CO-PW-FH-220	Trench Backfilling and Compaction Works for Fire Hydrants of Potable Water Network for	24	03-Mar-27	06-Mar-27	7,870	0	0	0	0%	0%
Irrigation Network		144	21-Feb-27	16-Mar-27	267,506	0	0	0	0%	0%
Main Line Pipes		144	21-Feb-27	16-Mar-27	267,506	0	0	0	0%	0%
CO-IR-ML-200	Trench Excavation and Bedding Works for Main Lines of Irrigation Network for	24	21-Feb-27	23-Feb-27	6,922	0	0	0	0%	0%
CO-IR-ML-210	Pipes Laying Works for Main Lines of Irrigation Network for Alignment-RD-02	24	28-Feb-27	02-Mar-27	34,609	0	0	0	0%	0%
CO-IR-ML-220	Installation Works for Main Line Valves of Irrigation Network for Alignment-RD-02	24	03-Mar-27	06-Mar-27	9,941	0	0	0	0%	0%
CO-IR-ML-230	Trench Backfilling and Compaction Works for Main Lines of Irrigation Network for	24	14-Mar-27	16-Mar-27	13,844	0	0	0	0%	0%
CO-IR-ML-240	Installation Works for Bulbblers And Sprinkler and Irrigation Control System of Irrigation	24	07-Mar-27	13-Mar-27	202,191	0	0	0	0%	0%
Medium Voltage Network		96	28-Mar-27	10-Apr-27	28,138	0	0	0	0%	0%
Cabling Works		96	28-Mar-27	10-Apr-27	28,138	0	0	0	0%	0%
CO-MV-ML-310	Trench Excavation and Bedding Works for Medium Voltage Network for Alignment-RD-02	32	28-Mar-27	31-Mar-27	6,170	0	0	0	0%	0%
CO-MV-ML-320	Duct Laying Works for Medium Voltage Network for Alignment-RD-02	32	01-Apr-27	05-Apr-27	15,103	0	0	0	0%	0%
CO-MV-ML-330	Trench Backfilling and Compaction Works for Medium Voltage Network for Alignment-RD-02	32	06-Apr-27	10-Apr-27	6,865	0	0	0	0%	0%
Low Voltage Network		320	17-Mar-27	02-May-27	139,309	0	0	0	0%	0%
Main Low Voltage Cables Works (Cable 300 MM)		280	17-Mar-27	26-Apr-27	70,049	0	0	0	0%	0%
CON-LV-ML-160	Trench Excavation and Bedding Works for Main Cable of Low Voltage Network for	40	11-Apr-27	15-Apr-27	13,675	0	0	0	0%	0%
CON-LV-ML-170	Cable Laying Works for Main Cable of Low Voltage Network for Alignment-RD-02	96	17-Mar-27	30-Mar-27	38,755	0	0	0	0%	0%
CON-LV-ML-180	Trench Backfilling and Compaction Works for Main Cable of Low Voltage Network for	72	17-Apr-27	26-Apr-27	17,619	0	0	0	0%	0%
Service Low Voltage Cables Works (Cable 70 MM)		112	17-Apr-27	02-May-27	63,213	0	0	0	0%	0%
CON-LV-HC-160	Trench Excavation and Bedding Works for Service Cable of Low Voltage Network for	32	17-Apr-27	20-Apr-27	6,839	0	0	0	0%	0%
CON-LV-HC-170	Cable Laying Works for Service Cable of Low Voltage Network for Alignment-RD-02	48	21-Apr-27	27-Apr-27	38,755	0	0	0	0%	0%
CON-LV-HC-180	Trench Backfilling and Compaction Works for Service Cable of Low Voltage Network for	32	28-Apr-27	02-May-27	17,619	0	0	0	0%	0%
Distribution Pillars Works		112	11-Apr-27	26-Apr-27	6,047	0	0	0	0%	0%
CON-LV-DP-160	Foundation Excavation Works for Distribution Pillars of Low Voltage Network for	48	11-Apr-27	17-Apr-27	2,281	0	0	0	0%	0%

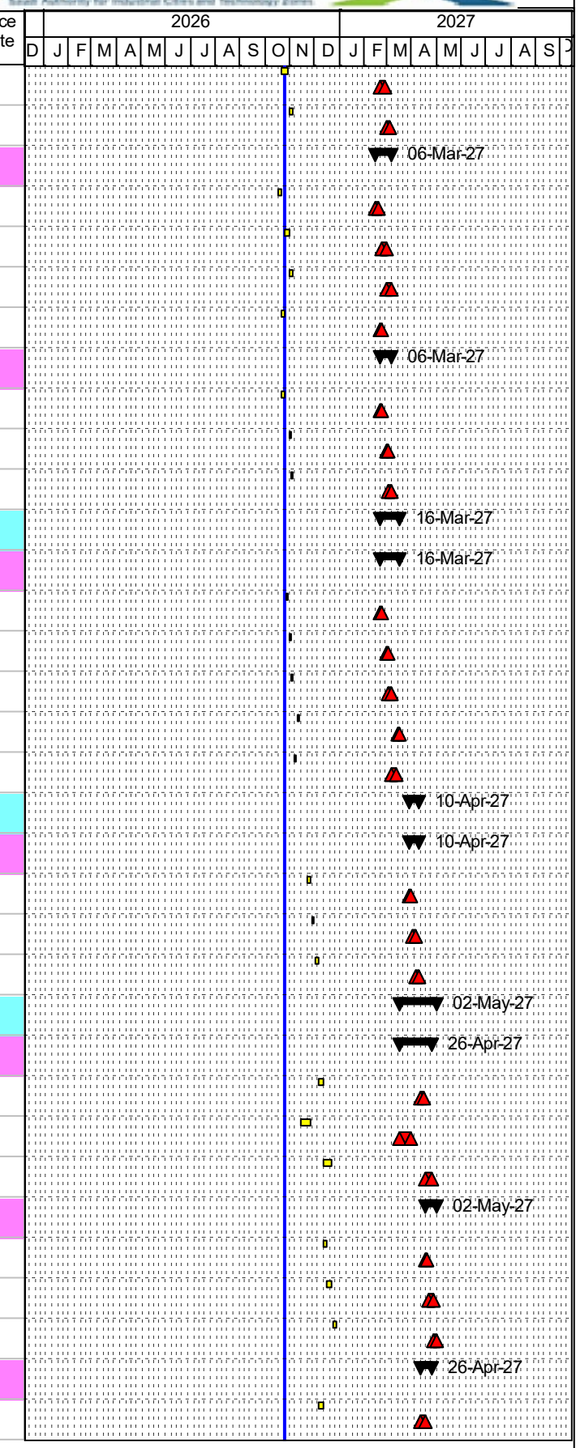

Primary Baseline | Actual Work | Summary
Remaining Work | Baseline Milestone
Critical Remaining Work | Milestone

Date	Revision	Checked	Approved
26-Oct-26	Third Industrial City		


Activity ID	Activity Name	Original Duration	Start	Finish	Budgeted Total Cost	Planned Value Cost	Earned Value Cost	Actual Total Cost	Schedule % Complete	Performance % Complete
CON-LV-DP-170	Pouring Plain Concrete For Distribution Pillar Units of Low Voltage Network for	32	18-Apr-27	21-Apr-27	1,883	0	0	0	0%	0%
CON-LV-DP-180	Installation Works for Distribution Pillar Units of Low Voltage Network for Alignment-RD-02	32	22-Apr-27	26-Apr-27	1,883	0	0	0	0%	0%
Street Lighting Network		168	18-Apr-27	11-May-27	123,598	0	0	0	0%	0%
Lighting Poles Works		88	18-Apr-27	29-Apr-27	44,088	0	0	0	0%	0%
CO-SL-LP-400	Installation Works for Lighting Poles Foundation of Street Lighting Network for	32	18-Apr-27	21-Apr-27	9,458	0	0	0	0%	0%
CO-SL-LP-410	Installation Works for Lighting Poles of Street Lighting Network for Alignment-RD-02	32	22-Apr-27	26-Apr-27	31,466	0	0	0	0%	0%
CO-SL-LP-430	Backfilling Works for Lighting Poles of Street Lighting Network for Alignment-RD-02	24	27-Apr-27	29-Apr-27	3,165	0	0	0	0%	0%
Cabling Works		56	18-Apr-27	25-Apr-27	62,968	0	0	0	0%	0%
CO-SL-CL-320	Cable Laying Works for Street Lighting Network for Alignment-RD-02	32	18-Apr-27	21-Apr-27	34,631	0	0	0	0%	0%
CO-SL-CL-330	Trench Backfilling and Compaction Works for Street Lighting Network for Alignment-RD-02	24	22-Apr-27	25-Apr-27	28,337	0	0	0	0%	0%
Distrubution Panel Boards		80	01-May-27	11-May-27	16,541	0	0	0	0%	0%
CO-SL-DB-330	Installation Works for Panel Board Concrete Foundations of Street Lighting Network for	24	01-May-27	03-May-27	3,545	0	0	0	0%	0%
CO-SL-DB-340	Installation Works for Lighting Panel Boards of Street Lighting Network for Alignment-RD-02	56	04-May-27	11-May-27	12,997	0	0	0	0%	0%
Telecom and Light Current Network		296	11-Apr-27	29-May-27	650,864	0	0	0	0%	0%
Ducts Works		80	12-May-27	29-May-27	116,180	0	0	0	0%	0%
CO-TE-DW-190	Pipes Laying Works for Ducts of Telecom Network for Alignment-RD-02	40	12-May-27	23-May-27	79,875	0	0	0	0%	0%
CO-TE-DW-200	Trench Backfilling and Compaction Works for Ducts of Telecom Network for	40	24-May-27	29-May-27	36,306	0	0	0	0%	0%
Manholes Works		72	11-Apr-27	20-Apr-27	30,612	0	0	0	0%	0%
CO-TE-MH-200	Excavation Works for Manholes of Telecom Network for Alignment-RD-02	24	11-Apr-27	13-Apr-27	2,041	0	0	0	0%	0%
CO-TE-MH-210	Installation Works for Manholes of Telecom Network for Alignment-RD-02	24	14-Apr-27	17-Apr-27	22,449	0	0	0	0%	0%
CO-TE-MH-220	Backfilling Works for Manholes of Telecom Network for Alignment-RD-02	24	18-Apr-27	20-Apr-27	6,122	0	0	0	0%	0%
CCTV, Telephone, MSN, ACs System Works		48	21-Apr-27	27-Apr-27	504,071	0	0	0	0%	0%
CO-TE-CTV-180	Installation of CCTV, Telephone, ACS and MSN Systems Cables for Alignment-RD-02	48	21-Apr-27	27-Apr-27	504,071	0	0	0	0%	0%
Road Works		208	03-May-27	07-Jun-27	1,365,735	0	0	0	0%	0%
Pavement Works		112	03-May-27	24-May-27	1,338,540	0	0	0	0%	0%
CO-RD-PV-200	Fixing of Curbstone for Sidewalks Pavement for Alignment-RD-02	40	03-May-27	08-May-27	131,137	0	0	0	0%	0%
CO-RD-PV-210	Fixing of Interlock Tiles for Sidewalks Pavement for Alignment-RD-02	72	09-May-27	24-May-27	1,207,402	0	0	0	0%	0%
Traffic Signs Boards and Roads Marking		64	30-May-27	07-Jun-27	27,195	0	0	0	0%	0%
CO-RD-F-RM-200	Application of Road Marking Works For Road Works for Alignment-RD-02	32	30-May-27	02-Jun-27	17,728	0	0	0	0%	0%
CO-RD-F-TS-140	Installation Works of Traffic Signs Boards For Road Works for Alignment-RD-02	32	03-Jun-27	07-Jun-27	9,468	0	0	0	0%	0%
Finishes for Infrastructure Networks		456	11-Apr-27	21-Jun-27	883,500	0	0	0	0%	0%
Storm Drainage Network		240	12-May-27	21-Jun-27	359,891	0	0	0	0%	0%
Testing and Finishes		240	12-May-27	21-Jun-27	359,891	0	0	0	0%	0%
CO-SD-CB-TF-200	Testing Works for Catch Basins of Storm Drainage Network for Alignment-RD-02	48	06-Jun-27	12-Jun-27	33,846	0	0	0	0%	0%

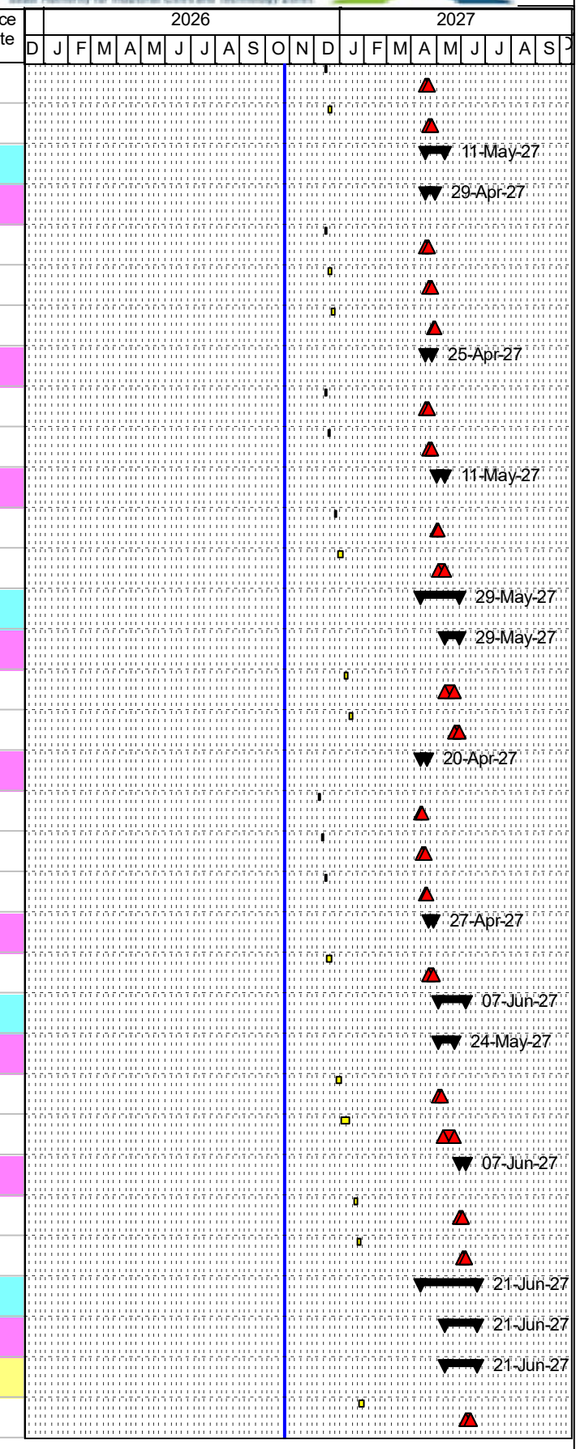

Primary Baseline | Actual Work | Summary
Remaining Work | Baseline Milestone
Critical Remaining Work | Milestone

Date	Revision	Checked	Approved
26-Oct-26	Third Industrial City		

Activity ID	Activity Name	Original Duration	Start	Finish	Budgeted Total Cost	Planned Value Cost	Earned Value Cost	Actual Total Cost	Schedule % Complete	Performance % Complete
CO-SD-CB-TF-210	Install Catch Basin Cover Works for External Finishes of Storm Drainage Network for	64	13-Jun-27	21-Jun-27	50,769	0	0	0	0%	0%
CO-SD-CB-TF-220	Catch Basin Internal Finishes (Benching) for Storm Drainage Network for Alignment-RD-02	48	30-May-27	05-Jun-27	50,769	0	0	0	0%	0%
CO-SD-MH-TF-250	Testing Works for Manholes of Storm Drainage Network for Alignment-RD-02	48	30-May-27	05-Jun-27	38,265	0	0	0	0%	0%
CO-SD-ML-TF-120	Testing Work for Pipes of Storm Drainage Network for Alignment-RD-02	48	12-May-27	24-May-27	186,241	0	0	0	0%	0%
Sewage Network		144	01-May-27	26-May-27	77,047	0	0	0	0%	0%
Testing and Finishes		144	01-May-27	26-May-27	77,047	0	0	0	0%	0%
CO-SW-TF-270	Final Testing For Main Line of Sewage Network for Alignment-RD-02	144	01-May-27	26-May-27	45,443	0	0	0	0%	0%
CO-SW-TF-290	Testing Works for Main Line Manholes of Sewage Network for Alignment-RD-02	144	01-May-27	26-May-27	31,604	0	0	0	0%	0%
Potable Water Network		240	27-Apr-27	06-Jun-27	102,331	0	0	0	0%	0%
Testing and Finishes		240	27-Apr-27	06-Jun-27	102,331	0	0	0	0%	0%
CO-PW-TF-160	Testing of Potable Water Network for Alignment-RD-02	64	29-May-27	06-Jun-27	28,291	0	0	0	0%	0%
CO-PW-TF-170	Fire Hydrant Finishies (S.Box + Safety + Marker Post) of Potable Water Network for	112	27-Apr-27	12-May-27	15,740	0	0	0	0%	0%
CO-PW-TF-180	Final Finishes works and Covers for Valves and Valve Chambers for Alignment-RD-02	64	13-May-27	27-May-27	58,301	0	0	0	0%	0%
Irrigation Network		32	09-May-27	12-May-27	13,844	0	0	0	0%	0%
Testing and Finishes		32	09-May-27	12-May-27	13,844	0	0	0	0%	0%
CO-IR-TF-180	Final Testing (pressure tests) of Irrigation Network for Alignment-RD-02	32	09-May-27	12-May-27	13,844	0	0	0	0%	0%
Treated Sewage Effluent (Tse)		48	30-May-27	05-Jun-27	77,686	0	0	0	0%	0%
Testing and Finishes		48	30-May-27	05-Jun-27	77,686	0	0	0	0%	0%
CO-TSE-TF-190	Final Testing (pressure tests) of Treated Sewage Effluent (Tse) for Alignment-RD-02	48	30-May-27	05-Jun-27	77,686	0	0	0	0%	0%
Medium Voltage Network		48	11-Apr-27	17-Apr-27	5,492	0	0	0	0%	0%
Termination and Testing Works		48	11-Apr-27	17-Apr-27	5,492	0	0	0	0%	0%
CO-MV-TF-240	Testing and Termination Works of Medium Voltage Network for Alignment-RD-02	48	11-Apr-27	17-Apr-27	5,492	0	0	0	0%	0%
Low Voltage Network		64	02-May-27	10-May-27	29,795	0	0	0	0%	0%
Termination and Testing Works		64	02-May-27	10-May-27	29,257	0	0	0	0%	0%
CON-LV-TT-140	Testing and Termination Works for Substation Low Voltage Panel Boards of Low Voltage	32	06-May-27	10-May-27	28,181	0	0	0	0%	0%
CON-LV-TT-150	Testing and Termination Works for Distribution Pillars Units of Low Voltage Network for	32	02-May-27	05-May-27	1,076	0	0	0	0%	0%
Earthing System Works		16	06-May-27	08-May-27	538	0	0	0	0%	0%
CON-LV-ES-120	Earthing System Works for Distribution Pillars Units of Low Voltage Network for	16	06-May-27	08-May-27	538	0	0	0	0%	0%
Street Lighting Network		128	04-May-27	27-May-27	52,148	0	0	0	0%	0%
Termination and Testing Works		128	04-May-27	27-May-27	46,478	0	0	0	0%	0%
CO-SL-LP-420	Installation Works for Lighting Fixtures With Drop Wire of Street Lighting Network for	16	04-May-27	05-May-27	20,510	0	0	0	0%	0%
CO-SL-TF-440	Termination Works For Panel Board Cables of Street Lighting Network for Alignment-RD-02	48	12-May-27	24-May-27	4,726	0	0	0	0%	0%
CO-SL-TF-450	Testing Works for Lighting Poles of Street Lighting Network for Alignment-RD-02	16	26-May-27	27-May-27	18,880	0	0	0	0%	0%
CO-SL-TF-460	Testing Works For Panel Board Cables of Street Lighting Network for Alignment-RD-02	16	26-May-27	27-May-27	2,363	0	0	0	0%	0%

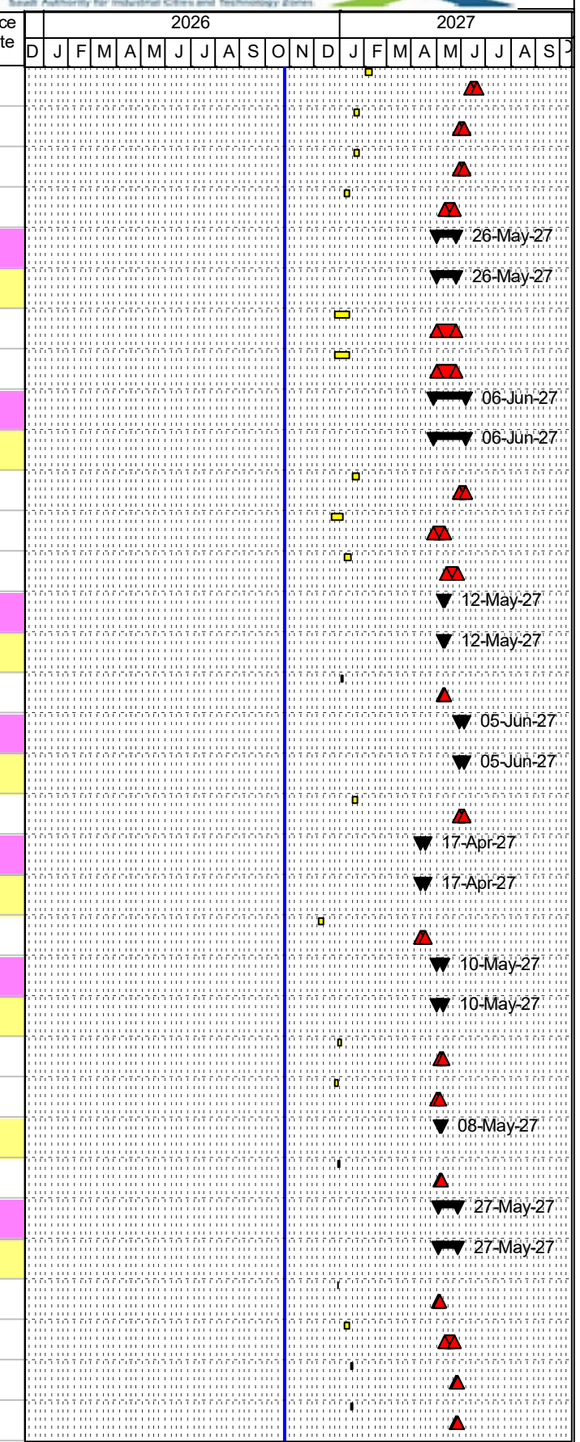


Primary Baseline | Actual Work | Summary
Remaining Work | Baseline Milestone
Critical Remaining Work | Milestone

Date	Revision	Checked	Approved
26-Oct-26	Third Industrial City		

Development of the Technology City in Dharan Project
BL-Update 26-10-2026
WPR UPS LEVEL 5

Activity ID	Activity Name	Original Duration	Start	Finish	Budgeted Total Cost	Planned Value Cost	Earned Value Cost	Actual Total Cost	Schedule % Complete	Performance % Complete
Earthing System Works		96	06-May-27	25-May-27	5,669	0	0	0	0%	0%
CO-SL-ES-260	Install Earthing System Works for Lighting Poles of Street Lighting Network for	48	06-May-27	12-May-27	2,835	0	0	0	0%	0%
CO-SL-ES-270	Install Earthing System Works for Lighting Panel Boards of Street Lighting Network for	48	13-May-27	25-May-27	2,835	0	0	0	0%	0%
Telecom and Light Current Network		48	06-May-27	12-May-27	165,267	0	0	0	0%	0%
Testing and Finishes		48	06-May-27	12-May-27	165,267	0	0	0	0%	0%
CO-TE-CTV-TF-220	Testing and Interface modules with Telecom for Alignment-RD-02	24	06-May-27	09-May-27	39,249	0	0	0	0%	0%
CO-TE-CTV-TF-350	Testing and Interface modules with CCTV, Telephone, MSN and Access Control for	24	10-May-27	12-May-27	126,018	0	0	0	0%	0%
Alignment-RD-03-1		1368	26-Oct-26	22-May-27	3,448,486	1,279,090	0	0	37.09%	0%
Earthworks		96	26-Oct-26	08-Nov-26	829,055	829,055	0	0	100%	0%
Earthworks		96	26-Oct-26	08-Nov-26	829,055	829,055	0	0	100%	0%
CO-EW-200	Excavation and Backfilling Works Upto Design Level for Earthworks for Alignment-RD-03-1	96	26-Oct-26	08-Nov-26	829,055	829,055	0	0	100%	0%
Storm Drainage Network		264	09-Nov-26	16-Dec-26	122,202	122,202	0	0	100%	0%
Manholes		264	09-Nov-26	16-Dec-26	48,644	48,644	0	0	100%	0%
CO-SD-MH-180	Trench Excavation and Bedding Works for Manholes of Storm Drainage Network for	80	09-Nov-26	19-Nov-26	3,243	3,243	0	0	100%	0%
CO-SD-MH-190	Install RC Footing Works for Manholes of Storm Drainage Network for	24	21-Nov-26	23-Nov-26	16,215	16,215	0	0	100%	0%
CO-SD-MH-200	Install RC Wall Rings & Slab Works for Manholes of Storm Drainage Network for	80	24-Nov-26	05-Dec-26	19,458	19,458	0	0	100%	0%
CO-SD-MH-220	Backfilling Works for Manholes of Storm Drainage Network for Alignment-RD-03-1	80	06-Dec-26	16-Dec-26	9,729	9,729	0	0	100%	0%
Main Line Sections		80	06-Dec-26	16-Dec-26	73,558	73,558	0	0	100%	0%
CO-SD-ML-100	Trench Excavation and Bedding Works for Main Lines of Storm Drainage Network for	24	06-Dec-26	08-Dec-26	9,196	9,196	0	0	100%	0%
CO-SD-ML-120	Pipes Laying Works for Main Lines of Storm Drainage Network for Alignment-RD-03-1	24	09-Dec-26	12-Dec-26	45,975	45,975	0	0	100%	0%
CO-SD-ML-130	Trench Backfilling and Compaction Works for Main Lines of Storm Drainage Network for	32	13-Dec-26	16-Dec-26	18,387	18,387	0	0	100%	0%
Treated Sewage Effluent (Tse)		952	24-Dec-26	20-May-27	880,133	273,530	0	0	31.08%	0%
CO-TSE-ML-150	Trench Excavation and Bedding Works for Main Lines of Treated Sewage Effluent (Tse)	32	24-Dec-26	28-Dec-26	4,681	4,681	0	0	100%	0%
CO-TSE-ML-160	Pipes Laying Works for Main Lines of Treated Sewage Effluent (Tse) for Alignment-RD-03-1	32	29-Dec-26	02-Jan-27	21,975	21,975	0	0	100%	0%
CO-TSE-ML-170	Installation Works for Main Line Valves of Treated Sewage Effluent (Tse) for	48	03-Jan-27	09-Jan-27	11,899	11,899	0	0	100%	0%
CO-TSE-ML-180	Trench Backfilling and Compaction Works for Treated Sewage Effluent (Tse) for	40	17-Jan-27	21-Jan-27	8,884	8,884	0	0	100%	0%
CO-TSE-ML-190	Installation Works for Valve and Washout Chambers of Treated Sewage Effluent (Tse)	48	10-Jan-27	16-Jan-27	226,089	226,089	0	0	100%	0%
Treated Sewage Effluent (Tse) Storage Tank		48	09-May-27	20-May-27	606,604	0	0	0	0%	0%
CO-TSE-TF-180	Installation of Storage Tank of Treated Sewage Effluent (Tse) for Alignment-RD-03-1	48	09-May-27	20-May-27	606,604	0	0	0	0%	0%
Potable Water Network		704	23-Jan-27	08-May-27	671,455	52,024	0	0	7.75%	0%
Main Line Sections		136	23-Jan-27	10-Feb-27	15,148	15,148	0	0	100%	0%
CO-PW-ML-100	Trench Excavation and Bedding Works for Main Lines of Potable Water Network for	40	23-Jan-27	27-Jan-27	2,765	2,765	0	0	100%	0%
CO-PW-ML-110	Pipes Laying and accessories for Main Lines of Potable Water Network for	40	28-Jan-27	02-Feb-27	6,878	6,878	0	0	100%	0%
CO-PW-ML-130	Trench Backfilling and Compaction Works for Main Lines of Potable Water Network for	56	03-Feb-27	10-Feb-27	5,505	5,505	0	0	100%	0%

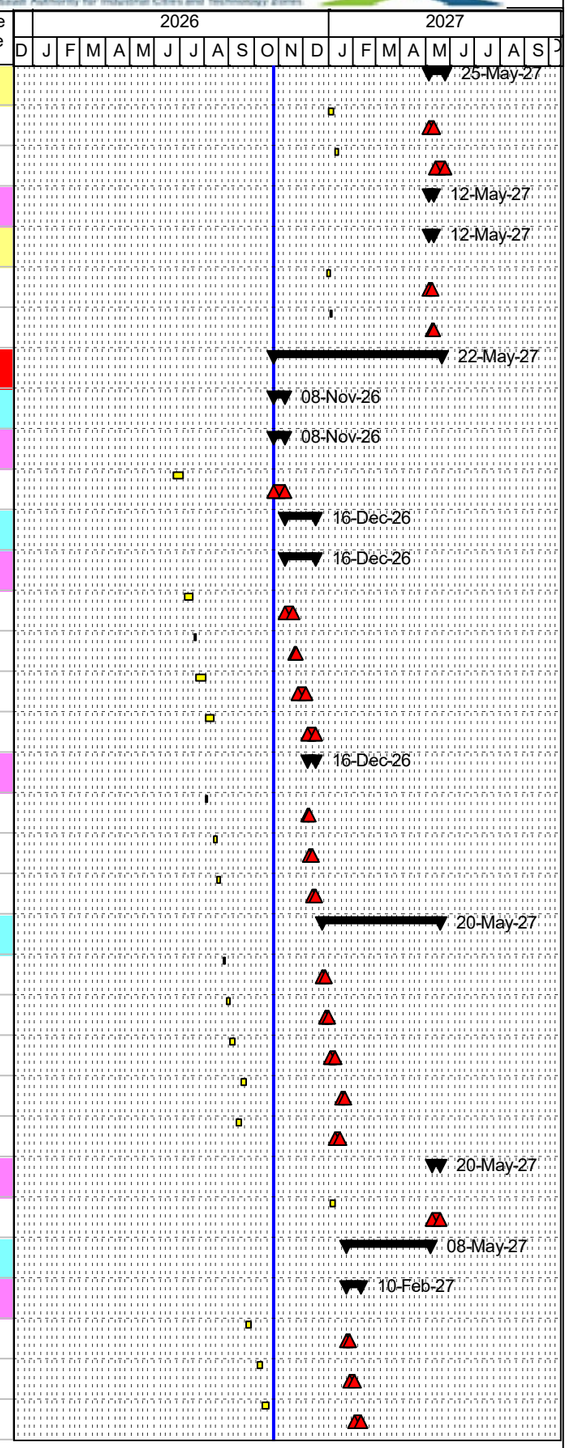


Primary Baseline | Actual Work | Summary
Remaining Work | Baseline Milestone
Critical Remaining Work | Milestone

Date	Revision	Checked	Approved
26-Oct-26	Third Industrial City		

Development of the Technology City in Dharan Project
BL-Update 26-10-2026
WPR UPS LEVEL 5

Activity ID	Activity Name	Original Duration	Start	Finish	Budgeted Total Cost	Planned Value Cost	Earned Value Cost	Actual Total Cost	Schedule % Complete	Performance % Complete
Valve Chamber		136	25-Jan-27	13-Feb-27	40,710	29,006	0	0	71.25%	0%
CO-PW-VC-170	Excavation Works for Main Line Valves and Valve Chambers of Potable Water Network for	24	25-Jan-27	27-Jan-27	2,544	2,544	0	0	100%	0%
CO-PW-VC-190	Installation Works for Valves of Potable Water Network for Alignment-RD-03-1	24	07-Feb-27	09-Feb-27	6,615	0	0	0	0%	0%
CO-PW-VC-220	Backfilling Works for Main Line Valves and Valve Chambers of Potable Water Network for	24	10-Feb-27	13-Feb-27	5,089	0	0	0	0%	0%
CO-PW-VC180	Installation of Valve Chambers of Potable Water Network for Alignment-RD-03-1	24	28-Jan-27	31-Jan-27	26,462	26,462	0	0	100%	0%
Fire Hydrant		112	28-Jan-27	13-Feb-27	8,994	7,870	0	0	87.5%	0%
CO-PW-FH-140	Excavation Works for Fire Hydrants of Potable Water Network for Alignment-RD-03-1	16	28-Jan-27	30-Jan-27	562	562	0	0	100%	0%
CO-PW-FH-150	Installation Works for Fire Hydrant of Potable Water Network for Alignment-RD-03-1	16	03-Feb-27	04-Feb-27	7,308	7,308	0	0	100%	0%
CO-PW-FH-160	Trench Backfilling and Compaction Works for Fire Hydrants of Potable Water Network for	16	11-Feb-27	13-Feb-27	1,124	0	0	0	0%	0%
Potable Water Network Storage Tank		48	02-May-27	08-May-27	606,604	0	0	0	0%	0%
CO-PW-TF-130	Installation of Storage Tank of Potable Water Network for Alignment-RD-03-1	48	02-May-27	08-May-27	606,604	0	0	0	0%	0%
Low Voltage Network		376	11-Feb-27	10-Apr-27	38,649	2,280	0	0	5.9%	0%
Main Low Voltage Cables Works (Cable 300 MM)		152	11-Feb-27	04-Mar-27	18,678	2,280	0	0	12.21%	0%
CON-LV-ML-100	Trench Excavation and Bedding Works for Main Cable of Low Voltage Network for	64	11-Feb-27	20-Feb-27	3,648	2,280	0	0	62.5%	0%
CON-LV-ML-110	Cable Laying Works for Main Cable of Low Voltage Network for Alignment-RD-03-1	56	21-Feb-27	28-Feb-27	10,333	0	0	0	0%	0%
CON-LV-ML-120	Trench Backfilling and Compaction Works for Main Cable of Low Voltage Network for	32	01-Mar-27	04-Mar-27	4,697	0	0	0	0%	0%
Service Low Voltage Cables Works (Cable 70 MM)		216	21-Feb-27	27-Mar-27	16,853	0	0	0	0%	0%
CON-LV-HC-100	Trench Excavation and Bedding Works for Service Cable of Low Voltage Network for	32	21-Feb-27	24-Feb-27	1,823	0	0	0	0%	0%
CON-LV-HC-110	Cable Laying Works for Service Cable of Low Voltage Network for Alignment-RD-03-1	56	16-Mar-27	23-Mar-27	10,333	0	0	0	0%	0%
CON-LV-HC-120	Trench Backfilling and Compaction Works for Service Cable of Low Voltage Network for	24	24-Mar-27	27-Mar-27	4,697	0	0	0	0%	0%
Distribution Pillars Works		96	28-Mar-27	10-Apr-27	3,119	0	0	0	0%	0%
CON-LV-DP-100	Foundation Excavation Works for Distribution Pillars of Low Voltage Network for	32	28-Mar-27	31-Mar-27	608	0	0	0	0%	0%
CON-LV-DP-110	Pouring Plain Concrete For Distribution Pillar Units of Low Voltage Network for	32	01-Apr-27	05-Apr-27	1,255	0	0	0	0%	0%
CON-LV-DP-120	Installation Works for Distribution Pillar Units of Low Voltage Network for Alignment-RD-03-1	32	06-Apr-27	10-Apr-27	1,255	0	0	0	0%	0%
Street Lighting Network		160	16-Mar-27	07-Apr-27	24,454	0	0	0	0%	0%
Lighting Poles Works		128	16-Mar-27	03-Apr-27	10,069	0	0	0	0%	0%
CO-SL-LP-550	Installation Works for Lighting Poles Foundation of Street Lighting Network for	40	16-Mar-27	21-Mar-27	2,158	0	0	0	0%	0%
CO-SL-LP-560	Installation Works for Lighting Poles of Street Lighting Network for Alignment-RD-03-1	40	22-Mar-27	27-Mar-27	7,192	0	0	0	0%	0%
CO-SL-LP-570	Backfilling Works for Lighting Poles of Street Lighting Network for Alignment-RD-03-1	48	28-Mar-27	03-Apr-27	719	0	0	0	0%	0%
Cabling Works		80	28-Mar-27	07-Apr-27	14,384	0	0	0	0%	0%
CO-SL-CL-410	Cable Laying Works for Street Lighting Network for Alignment-RD-03-1	40	28-Mar-27	01-Apr-27	7,911	0	0	0	0%	0%
CO-SL-CL-420	Trench Backfilling and Compaction Works for Street Lighting Network for Alignment-RD-03-1	40	03-Apr-27	07-Apr-27	6,473	0	0	0	0%	0%
Telecom and Light Current Network		96	04-Apr-27	17-Apr-27	234,558	0	0	0	0%	0%
Ducts Works		64	08-Apr-27	17-Apr-27	30,845	0	0	0	0%	0%

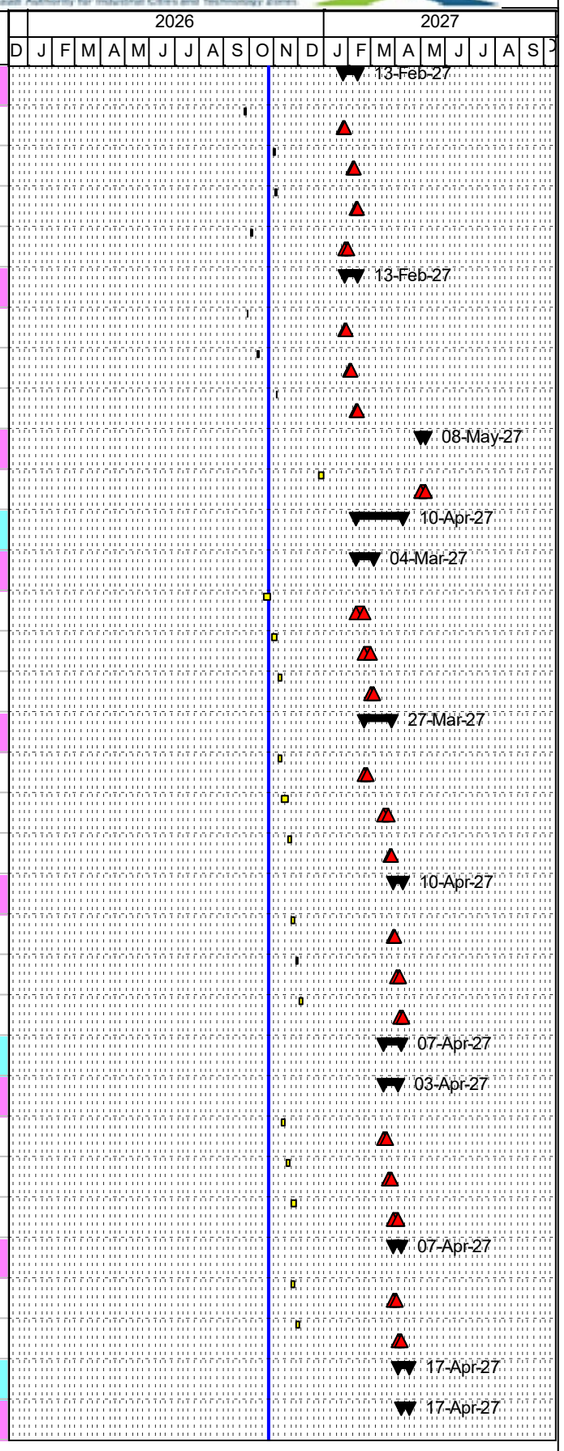


Primary Baseline | Actual Work | Summary
Remaining Work | Baseline Milestone
Critical Remaining Work | Milestone

Date	Revision	Checked	Approved
26-Oct-26	Third Industrial City		

Development of the Technology City in Dharan Project
BL-Update 26-10-2026
WPR UPS LEVEL 5


Activity ID	Activity Name	Original Duration	Start	Finish	Budgeted Total Cost	Planned Value Cost	Earned Value Cost	Actual Total Cost	Schedule % Complete	Performance % Complete
CO-TE-DW-110	Pipes Laying Works for Ducts of Telecom Network for Alignment-RD-03-1	32	08-Apr-27	12-Apr-27	21,205	0	0	0	0%	0%
CO-TE-DW-130	Trench Backfilling and Compaction Works for Ducts of Telecom Network for	32	13-Apr-27	17-Apr-27	9,640	0	0	0	0%	0%
Manholes Works		48	04-Apr-27	10-Apr-27	14,687	0	0	0	0%	0%
CO-TE-MH-140	Excavation Works for Manholes of Telecom Network for Alignment-RD-03-1	16	04-Apr-27	05-Apr-27	979	0	0	0	0%	0%
CO-TE-MH-150	Installation Works for Manholes of Telecom Network for Alignment-RD-03-1	16	06-Apr-27	07-Apr-27	10,770	0	0	0	0%	0%
CO-TE-MH-160	Backfilling Works for Manholes of Telecom Network for Alignment-RD-03-1	16	08-Apr-27	10-Apr-27	2,937	0	0	0	0%	0%
CCTV, Telephone, MSN, ACs System Works		32	11-Apr-27	14-Apr-27	189,027	0	0	0	0%	0%
CO-TE-CTV-110	Installation of CCTV, Telephone, ACS and MSN Systems Cables for Alignment-RD-03-1	32	11-Apr-27	14-Apr-27	189,027	0	0	0	0%	0%
Road Works		176	18-Apr-27	12-May-27	499,484	0	0	0	0%	0%
Pre-Bituminous Construction		112	18-Apr-27	03-May-27	134,372	0	0	0	0%	0%
CO-RD-PB-140	Subgrade Layer for Road Works for Alignment-RD-03-1	56	18-Apr-27	25-Apr-27	65,548	0	0	0	0%	0%
CO-RD-PB-150	Aggregate Base Course Layer for Road Works for Alignment-RD-03-1	56	26-Apr-27	03-May-27	68,824	0	0	0	0%	0%
Bituminous Construction		56	26-Apr-27	03-May-27	278,096	0	0	0	0%	0%
CO-RD-B-160	Bituminous Base Courses Layers for Road Works for Alignment-RD-03-1	16	26-Apr-27	27-Apr-27	138,392	0	0	0	0%	0%
CON-RD-MR-150	Preparation of Asphaltic Wearing Course Layer for Roads Network for	16	02-May-27	03-May-27	139,704	0	0	0	0%	0%
Pavement Works		104	28-Apr-27	12-May-27	75,922	0	0	0	0%	0%
CO-RD-PV-160	Fixing of Curbstone for Sidewalks Pavement for Alignment-RD-03-1	40	28-Apr-27	03-May-27	46,267	0	0	0	0%	0%
CO-RD-PV-170	Fixing of Interlock Tiles for Sidewalks Pavement for Alignment-RD-03-1	64	04-May-27	12-May-27	29,656	0	0	0	0%	0%
Traffic Signs Boards and Roads Marking		32	04-May-27	08-May-27	11,093	0	0	0	0%	0%
CO-RD-F-RM-180	Application of Road Marking Works For Road Works for Alignment-RD-03-1	16	04-May-27	05-May-27	6,360	0	0	0	0%	0%
CO-RD-F-TS-120	Installation Works of Traffic Signs Boards For Road Works for Alignment-RD-03-1	16	06-May-27	08-May-27	4,734	0	0	0	0%	0%
Finishes for Infrastructure Networks		248	11-Apr-27	22-May-27	148,496	0	0	0	0%	0%
Storm Drainage Network		48	01-May-27	06-May-27	34,602	0	0	0	0%	0%
Testing and Finishes		48	01-May-27	06-May-27	34,602	0	0	0	0%	0%
CO-SD-MH-TF-210	Testing Works for Manholes of Storm Drainage Network for Alignment-RD-03-1	24	04-May-27	06-May-27	16,215	0	0	0	0%	0%
CO-SD-ML-TF-100	Testing Work for Pipes of Storm Drainage Network for Alignment-RD-03-1	24	01-May-27	03-May-27	18,387	0	0	0	0%	0%
Potable Water Network		32	27-Apr-27	01-May-27	24,809	0	0	0	0%	0%
Testing and Finishes		32	27-Apr-27	01-May-27	24,809	0	0	0	0%	0%
CO-PW-TF-100	Final Finishes works and Covers for Valves and Valve Chambers for Alignment-RD-03-1	32	27-Apr-27	01-May-27	17,055	0	0	0	0%	0%
CO-PW-TF-110	Testing of Potable Water Network for Alignment-RD-03-1	16	27-Apr-27	28-Apr-27	5,505	0	0	0	0%	0%
CO-PW-TF-120	Fire Hydrant Finishies (S.Box + Safety + Marker Post) of Potable Water Network for	24	27-Apr-27	29-Apr-27	2,249	0	0	0	0%	0%
Treated Sewage Effluent (Tse)		8	22-May-27	22-May-27	8,884	0	0	0	0%	0%
Testing and Finishes		8	22-May-27	22-May-27	8,884	0	0	0	0%	0%
CO-TSE-TF-170	Final Testing (pressure tests) of Treated Sewage Effluent (Tse) for Alignment-RD-03-1	8	22-May-27	22-May-27	8,884	0	0	0	0%	0%

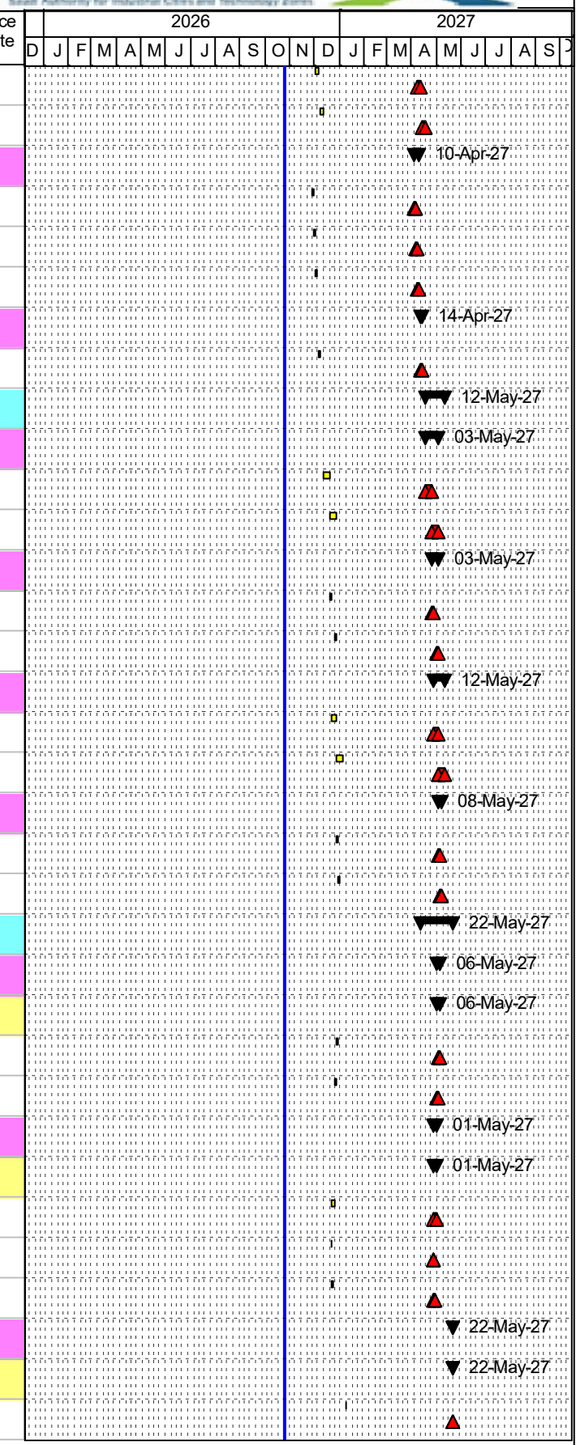

Primary Baseline
Remaining Work
Critical Remaining Work
Actual Work
Baseline Milestone
Milestone
Summary

Date	Revision	Checked	Approved
26-Oct-26	Third Industrial City		

Activity ID	Activity Name	Original Duration	Start	Finish	Budgeted Total Cost	Planned Value Cost	Earned Value Cost	Actual Total Cost	Schedule % Complete	Performance % Complete
Low Voltage Network		32	11-Apr-27	14-Apr-27	8,591	0	0	0	0%	0%
Termination and Testing Works		32	11-Apr-27	14-Apr-27	8,232	0	0	0	0%	0%
CON-LV-TT-100	Testing and Termination Works for Substation Low Voltage Panel Boards of Low Voltage	16	13-Apr-27	14-Apr-27	7,515	0	0	0	0%	0%
CON-LV-TT-110	Testing and Termination Works for Distribution Pillars Units of Low Voltage Network for	16	11-Apr-27	12-Apr-27	717	0	0	0	0%	0%
Earthing System Works		16	13-Apr-27	14-Apr-27	359	0	0	0	0%	0%
CON-LV-ES-100	Earthing System Works for Distribution Pillars Units of Low Voltage Network for	16	13-Apr-27	14-Apr-27	359	0	0	0	0%	0%
Street Lighting Network		136	20-Apr-27	09-May-27	10,034	0	0	0	0%	0%
Termination and Testing Works		136	20-Apr-27	09-May-27	9,003	0	0	0	0%	0%
CO-SL-LP-580	Installation Works for Lighting Fixtures With Drop Wire of Street Lighting Network for	48	20-Apr-27	26-Apr-27	4,688	0	0	0	0%	0%
CO-SL-TF-570	Testing Works for Lighting Poles of Street Lighting Network for Alignment-RD-03-1	48	03-May-27	09-May-27	4,315	0	0	0	0%	0%
Earthing System Works		40	27-Apr-27	02-May-27	1,031	0	0	0	0%	0%
CO-SL-ES-320	Install Earthing System Works for Lighting Poles of Street Lighting Network for	24	27-Apr-27	29-Apr-27	515	0	0	0	0%	0%
CO-SL-ES-330	Install Earthing System Works for Lighting Panel Boards of Street Lighting Network for	16	01-May-27	02-May-27	515	0	0	0	0%	0%
Telecom and Light Current Network		48	15-Apr-27	21-Apr-27	61,576	0	0	0	0%	0%
Testing and Finishes		48	15-Apr-27	21-Apr-27	61,576	0	0	0	0%	0%
CO-TE-CTV-TF-140	Testing and Interface modules with Telecom for Alignment-RD-03-1	48	15-Apr-27	21-Apr-27	12,607	0	0	0	0%	0%
CO-TE-CTV-TF-330	Testing and Interface modules with CCTV, Telephone, MSN and Access Control for	48	15-Apr-27	21-Apr-27	48,969	0	0	0	0%	0%
Alignment-RD-03-2		1536	28-Oct-26	17-Jun-27	3,959,670	2,215,741	0	0	55.96%	0%
Earthworks		96	28-Oct-26	10-Nov-26	1,830,833	1,830,833	0	0	100%	0%
Earthworks		96	28-Oct-26	10-Nov-26	1,830,833	1,830,833	0	0	100%	0%
CO-EW-240	Excavation and Backfilling Works Upto Design Level for Earthworks for Alignment-RD-03-2	96	28-Oct-26	10-Nov-26	1,830,833	1,830,833	0	0	100%	0%
Storm Drainage Network		376	17-Dec-26	09-Feb-27	384,908	384,908	0	0	100%	0%
Manholes		288	17-Dec-26	27-Jan-27	163,658	163,658	0	0	100%	0%
CO-SD-MH-350	Trench Excavation and Bedding Works for Manholes of Storm Drainage Network for	80	17-Dec-26	28-Dec-26	10,911	10,911	0	0	100%	0%
CO-SD-MH-360	Install RC Footing Works for Manholes of Storm Drainage Network for	72	29-Dec-26	07-Jan-27	54,553	54,553	0	0	100%	0%
CO-SD-MH-370	Install RC Wall Rings & Slab Works for Manholes of Storm Drainage Network for	80	09-Jan-27	19-Jan-27	65,463	65,463	0	0	100%	0%
CO-SD-MH-380	Backfilling Works for Manholes of Storm Drainage Network for Alignment-RD-03-2	56	20-Jan-27	27-Jan-27	32,732	32,732	0	0	100%	0%
Main Line Sections		144	20-Jan-27	09-Feb-27	221,251	221,251	0	0	100%	0%
CO-SD-ML-230	Trench Excavation and Bedding Works for Main Lines of Storm Drainage Network for	56	20-Jan-27	27-Jan-27	39,655	39,655	0	0	100%	0%
CO-SD-ML-240	Pipes Laying Works for Main Lines of Storm Drainage Network for Alignment-RD-03-2	40	28-Jan-27	02-Feb-27	126,283	126,283	0	0	100%	0%
CO-SD-ML-250	Trench Backfilling and Compaction Works for Main Lines of Storm Drainage Network for	48	03-Feb-27	09-Feb-27	55,313	55,313	0	0	100%	0%
Medium Voltage Network		128	07-Mar-27	28-Mar-27	25,481	0	0	0	0%	0%
Cabling Works		128	07-Mar-27	28-Mar-27	25,481	0	0	0	0%	0%
CO-MV-ML-370	Trench Excavation and Bedding Works for Medium Voltage Network for	40	07-Mar-27	15-Mar-27	5,553	0	0	0	0%	0%

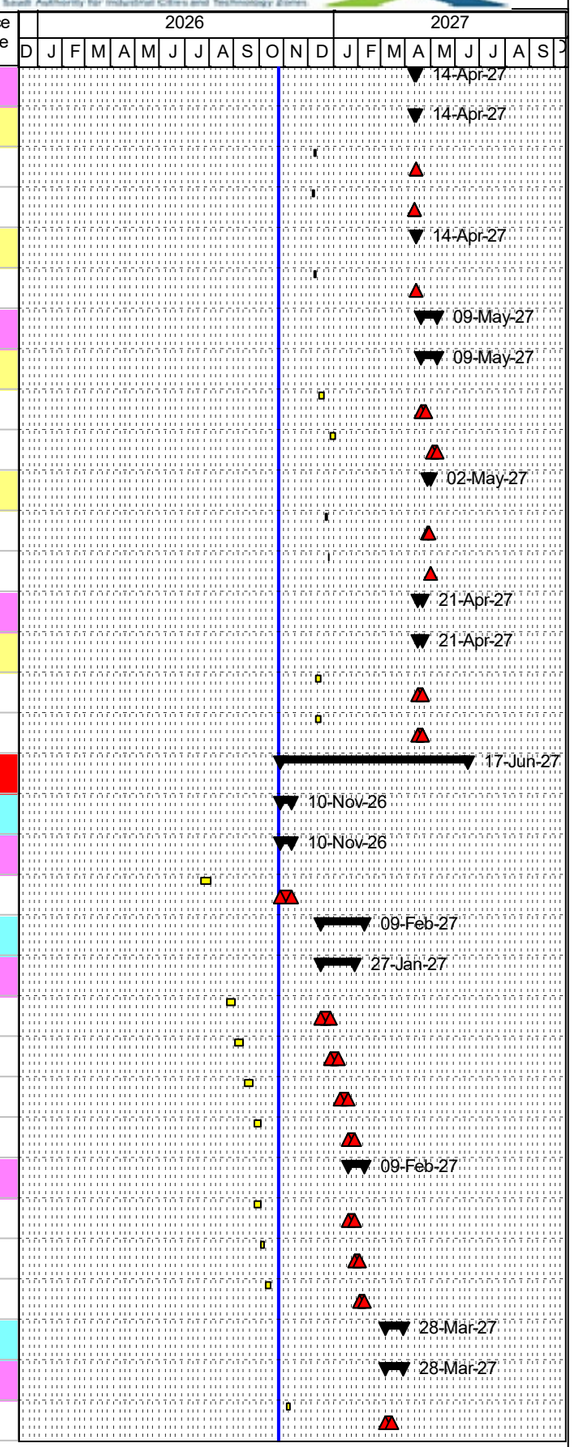


Primary Baseline | Actual Work | Summary
Remaining Work | Baseline Milestone
Critical Remaining Work | Milestone

Date	Revision	Checked	Approved
26-Oct-26	Third Industrial City		

Development of the Technology City in Dharan Project
BL-Update 26-10-2026
WPR UPS LEVEL 5


Activity ID	Activity Name	Original Duration	Start	Finish	Budgeted Total Cost	Planned Value Cost	Earned Value Cost	Actual Total Cost	Schedule % Complete	Performance % Complete
CO-MV-ML-380	Duct Laying Works for Medium Voltage Network for Alignment-RD-03-2	40	17-Mar-27	22-Mar-27	13,701	0	0	0	0%	0%
CO-MV-ML-390	Trench Backfilling and Compaction Works for Medium Voltage Network for	32	24-Mar-27	28-Mar-27	6,228	0	0	0	0%	0%
Low Voltage Network		240	31-Mar-27	04-May-27	82,593	0	0	0	0%	0%
Main Low Voltage Cables Works (Cable 300 MM)		168	31-Mar-27	24-Apr-27	42,036	0	0	0	0%	0%
CON-LV-ML-220	Trench Excavation and Bedding Works for Main Cable of Low Voltage Network for	48	31-Mar-27	06-Apr-27	8,206	0	0	0	0%	0%
CON-LV-ML-230	Cable Laying Works for Main Cable of Low Voltage Network for Alignment-RD-03-2	72	07-Apr-27	17-Apr-27	23,255	0	0	0	0%	0%
CON-LV-ML-240	Trench Backfilling and Compaction Works for Main Cable of Low Voltage Network for	48	18-Apr-27	24-Apr-27	10,574	0	0	0	0%	0%
Service Low Voltage Cables Works (Cable 70 MM)		192	07-Apr-27	04-May-27	37,933	0	0	0	0%	0%
CON-LV-HC-220	Trench Excavation and Bedding Works for Service Cable of Low Voltage Network for	40	07-Apr-27	12-Apr-27	4,104	0	0	0	0%	0%
CON-LV-HC-230	Cable Laying Works for Service Cable of Low Voltage Network for Alignment-RD-03-2	72	18-Apr-27	27-Apr-27	23,255	0	0	0	0%	0%
CON-LV-HC-240	Trench Backfilling and Compaction Works for Service Cable of Low Voltage Network for	48	28-Apr-27	04-May-27	10,574	0	0	0	0%	0%
Distribution Pillars Works		88	08-Apr-27	20-Apr-27	2,624	0	0	0	0%	0%
CON-LV-DP-220	Foundation Excavation Works for Distribution Pillars of Low Voltage Network for	56	08-Apr-27	15-Apr-27	1,369	0	0	0	0%	0%
CON-LV-DP-230	Pouring Plain Concrete For Distribution Pillar Units of Low Voltage Network for	16	17-Apr-27	18-Apr-27	628	0	0	0	0%	0%
CON-LV-DP-240	Installation Works for Distribution Pillar Units of Low Voltage Network for Alignment-RD-03-2	16	19-Apr-27	20-Apr-27	628	0	0	0	0%	0%
Street Lighting Network		168	16-Mar-27	08-Apr-27	55,021	0	0	0	0%	0%
Lighting Poles Works		128	16-Mar-27	03-Apr-27	22,656	0	0	0	0%	0%
CO-SL-LP-500	Installation Works for Lighting Poles Foundation of Street Lighting Network for	40	16-Mar-27	21-Mar-27	4,855	0	0	0	0%	0%
CO-SL-LP-510	Installation Works for Lighting Poles of Street Lighting Network for Alignment-RD-03-2	40	22-Mar-27	27-Mar-27	16,183	0	0	0	0%	0%
CO-SL-LP-520	Backfilling Works for Lighting Poles of Street Lighting Network for Alignment-RD-03-2	48	28-Mar-27	03-Apr-27	1,618	0	0	0	0%	0%
Cabling Works		80	29-Mar-27	08-Apr-27	32,365	0	0	0	0%	0%
CO-SL-CL-380	Cable Laying Works for Street Lighting Network for Alignment-RD-03-2	40	29-Mar-27	03-Apr-27	17,801	0	0	0	0%	0%
CO-SL-CL-390	Trench Backfilling and Compaction Works for Street Lighting Network for Alignment-RD-03-2	40	04-Apr-27	08-Apr-27	14,564	0	0	0	0%	0%
Telecom and Light Current Network		24	05-May-27	08-May-27	252,036	0	0	0	0%	0%
CCTV, Telephone, MSN, ACs System Works		24	05-May-27	08-May-27	252,036	0	0	0	0%	0%
CO-TE-CTV-240	Installation of CCTV, Telephone, ACS and MSN Systems Cables for Alignment-RD-03-2	24	05-May-27	08-May-27	252,036	0	0	0	0%	0%
Road Works		264	05-May-27	17-Jun-27	1,110,832	0	0	0	0%	0%
Pre-Bituminous Construction		80	05-May-27	22-May-27	299,699	0	0	0	0%	0%
CO-RD-PB-220	Subgrade Layer for Road Works for Alignment-RD-03-2	40	05-May-27	10-May-27	146,196	0	0	0	0%	0%
CO-RD-PB-230	Installation of Aggregate Base Course Layer and Interlock Works for Road Works for	40	11-May-27	22-May-27	153,503	0	0	0	0%	0%
Bituminous Construction		120	23-May-27	08-Jun-27	620,266	0	0	0	0%	0%
CO-RD-B-240	Bituminous Base Courses Layers for Road Works for Alignment-RD-03-2	24	23-May-27	25-May-27	308,669	0	0	0	0%	0%
CON-RD-MR-230	Preparation of Asphaltic Wearing Course Layer for Roads Network for	24	06-Jun-27	08-Jun-27	311,597	0	0	0	0%	0%
Pavement Works		112	26-May-27	10-Jun-27	169,336	0	0	0	0%	0%

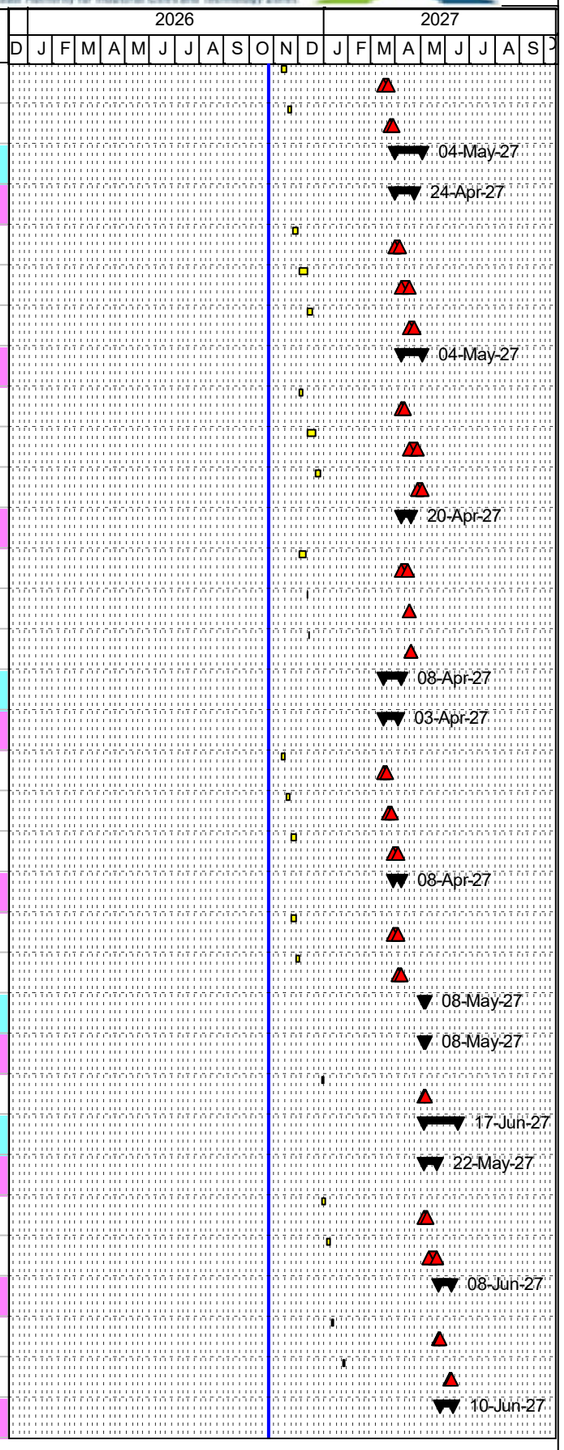

Primary Baseline | Actual Work | Summary
Remaining Work | Baseline Milestone
Critical Remaining Work | Milestone

Date	Revision	Checked	Approved
26-Oct-26	Third Industrial City		

Activity ID	Activity Name	Original Duration	Start	Finish	Budgeted Total Cost	Planned Value Cost	Earned Value Cost	Actual Total Cost	Schedule % Complete	Performance % Complete
CO-RD-PV-240	Fixing of Curbstone for Sidewalks Pavement for Alignment-RD-03-2	56	26-May-27	02-Jun-27	103,193	0	0	0	0%	0%
CO-RD-PV-250	Fixing of Interlock Tiles for Sidewalks Pavement for Alignment-RD-03-2	56	03-Jun-27	10-Jun-27	66,143	0	0	0	0%	0%
Traffic Signs Boards and Roads Marking		48	12-Jun-27	17-Jun-27	21,532	0	0	0	0%	0%
CO-RD-F-RM-220	Application of Road Marking Works For Road Works for Alignment-RD-03-2	24	12-Jun-27	14-Jun-27	13,958	0	0	0	0%	0%
CO-RD-F-TS-160	Installation Works of Traffic Signs Boards For Road Works for Alignment-RD-03-2	24	15-Jun-27	17-Jun-27	7,574	0	0	0	0%	0%
Finishes for Infrastructure Networks		432	29-Mar-27	05-Jun-27	217,965	0	0	0	0%	0%
Storm Drainage Network		128	12-May-27	05-Jun-27	109,865	0	0	0	0%	0%
Testing and Finishes		128	12-May-27	05-Jun-27	109,865	0	0	0	0%	0%
CO-SD-CB-TF-260	Testing Works for Catch Basins of Storm Drainage Network for Alignment-RD-03-2	72	26-May-27	05-Jun-27	55,313	0	0	0	0%	0%
CO-SD-MH-TF-290	Testing Works for Manholes of Storm Drainage Network for Alignment-RD-03-2	48	12-May-27	24-May-27	54,553	0	0	0	0%	0%
Medium Voltage Network		48	29-Mar-27	04-Apr-27	4,982	0	0	0	0%	0%
Termination and Testing Works		48	29-Mar-27	04-Apr-27	4,982	0	0	0	0%	0%
CO-MV-TF-260	Testing and Termination Works of Medium Voltage Network for Alignment-RD-03-2	48	29-Mar-27	04-Apr-27	4,982	0	0	0	0%	0%
Low Voltage Network		152	21-Apr-27	12-May-27	17,446	0	0	0	0%	0%
Termination and Testing Works		152	21-Apr-27	12-May-27	17,267	0	0	0	0%	0%
CON-LV-TT-180	Testing and Termination Works for Substation Low Voltage Panel Boards of Low Voltage	56	05-May-27	12-May-27	16,908	0	0	0	0%	0%
CON-LV-TT-190	Testing and Termination Works for Distribution Pillars Units of Low Voltage Network for	48	21-Apr-27	27-Apr-27	359	0	0	0	0%	0%
Earthing System Works		16	28-Apr-27	29-Apr-27	179	0	0	0	0%	0%
CON-LV-ES-140	Earthing System Works for Distribution Pillars Units of Low Voltage Network for	16	28-Apr-27	29-Apr-27	179	0	0	0	0%	0%
Street Lighting Network		120	13-Apr-27	29-Apr-27	22,662	0	0	0	0%	0%
Termination and Testing Works		120	13-Apr-27	29-Apr-27	20,257	0	0	0	0%	0%
CO-SL-LP-530	Installation Works for Lighting Fixtures With Drop Wire of Street Lighting Network for	48	13-Apr-27	19-Apr-27	10,548	0	0	0	0%	0%
CO-SL-TF-530	Testing Works for Lighting Poles of Street Lighting Network for Alignment-RD-03-2	48	24-Apr-27	29-Apr-27	9,710	0	0	0	0%	0%
Earthing System Works		40	24-Apr-27	28-Apr-27	2,405	0	0	0	0%	0%
CO-SL-ES-300	Install Earthing System Works for Lighting Poles of Street Lighting Network for	24	24-Apr-27	26-Apr-27	1,203	0	0	0	0%	0%
CO-SL-ES-310	Install Earthing System Works for Lighting Panel Boards of Street Lighting Network for	16	27-Apr-27	28-Apr-27	1,203	0	0	0	0%	0%
Telecom and Light Current Network		32	09-May-27	12-May-27	63,009	0	0	0	0%	0%
Testing and Finishes		32	09-May-27	12-May-27	63,009	0	0	0	0%	0%
CO-TE-CTV-TF-320	Testing and Interface modules with CCTV, Telephone, MSN and Access Control for	32	09-May-27	12-May-27	63,009	0	0	0	0%	0%
Alignment-RD-03-3		1320	09-Nov-26	29-May-27	2,245,578	1,111,105	0	0	49.48%	0%
Earthworks		88	09-Nov-26	21-Nov-26	1,036,317	1,036,317	0	0	100%	0%
Earthworks		88	09-Nov-26	21-Nov-26	1,036,317	1,036,317	0	0	100%	0%
CO-EW-230	Excavation and Backfilling Works Upto Design Level for Earthworks for Alignment-RD-03-3	88	09-Nov-26	21-Nov-26	1,036,317	1,036,317	0	0	100%	0%
Storm Drainage Network		80	09-Dec-26	20-Dec-26	38,627	38,627	0	0	100%	0%

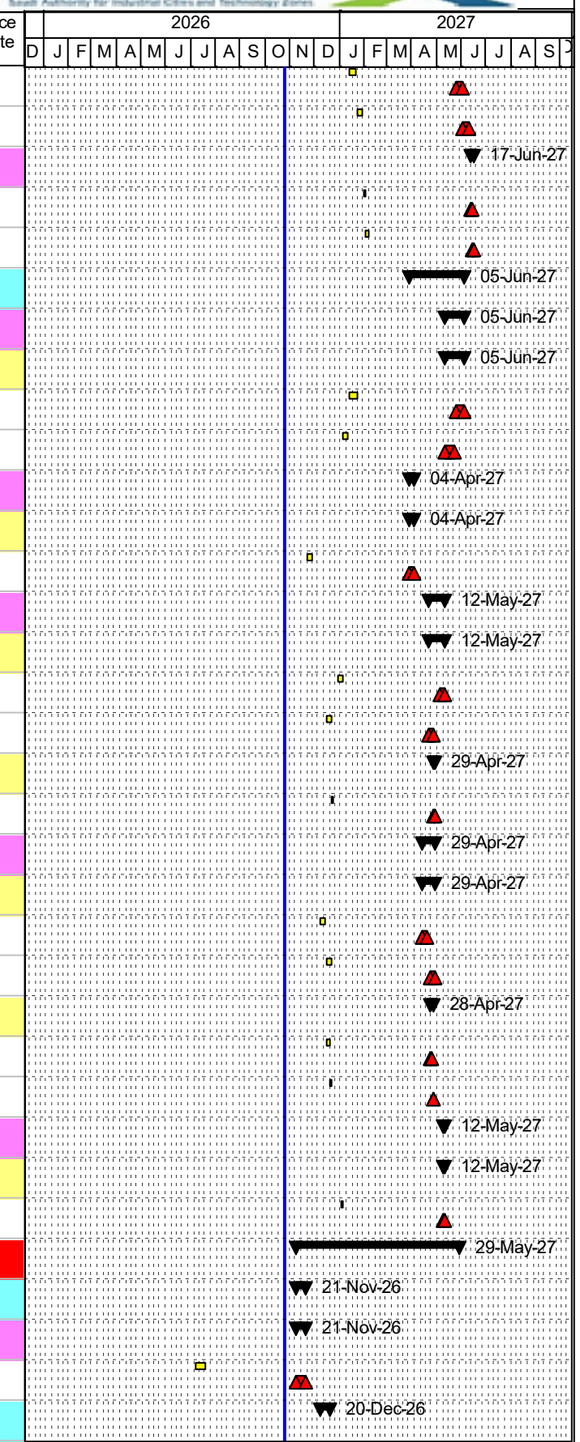


Primary Baseline | Actual Work | Summary
Remaining Work | Baseline Milestone
Critical Remaining Work | Milestone

Date	Revision	Checked	Approved
26-Oct-26	Third Industrial City		

Development of the Technology City in Dharan Project
BL-Update 26-10-2026
WPR UPS LEVEL 5

Activity ID	Activity Name	Original Duration	Start	Finish	Budgeted Total Cost	Planned Value Cost	Earned Value Cost	Actual Total Cost	Schedule % Complete	Performance % Complete
Main Line Sections		80	09-Dec-26	20-Dec-26	38,627	38,627	0	0	100%	0%
CO-SD-ML-200	Trench Excavation and Bedding Works for Main Lines of Storm Drainage Network for	24	09-Dec-26	12-Dec-26	4,830	4,830	0	0	100%	0%
CO-SD-ML-210	Pipes Laying Works for Main Lines of Storm Drainage Network for Alignment-RD-03-3	24	13-Dec-26	15-Dec-26	24,141	24,141	0	0	100%	0%
CO-SD-ML-220	Trench Backfilling and Compaction Works for Main Lines of Storm Drainage Network for	24	17-Dec-26	20-Dec-26	9,656	9,656	0	0	100%	0%
Treated Sewage Effluent (Tse)		264	21-Dec-26	27-Jan-27	6,040	6,040	0	0	100%	0%
CO-TSE-ML-300	Trench Excavation and Bedding Works for Main Lines of Treated Sewage Effluent (Tse)	88	21-Dec-26	02-Jan-27	755	755	0	0	100%	0%
CO-TSE-ML-310	Pipes Laying Works for Main Lines of Treated Sewage Effluent (Tse) for Alignment-RD-03-3	88	03-Jan-27	14-Jan-27	3,775	3,775	0	0	100%	0%
CO-TSE-ML-330	Trench Backfilling and Compaction Works for Treated Sewage Effluent (Tse) for	88	16-Jan-27	27-Jan-27	1,510	1,510	0	0	100%	0%
Potable Water Network		256	28-Jan-27	06-Mar-27	53,061	28,045	0	0	52.85%	0%
Main Line Sections		240	28-Jan-27	03-Mar-27	17,558	10,375	0	0	59.09%	0%
CO-PW-ML-200	Trench Excavation and Bedding Works for Main Lines of Potable Water Network for	80	28-Jan-27	08-Feb-27	3,191	3,191	0	0	100%	0%
CO-PW-ML-210	Pipes Laying and accessories for Main Lines of Potable Water Network for	80	09-Feb-27	20-Feb-27	7,981	7,183	0	0	90%	0%
CO-PW-ML-220	Trench Backfilling and Compaction Works for Main Lines of Potable Water Network for	80	21-Feb-27	03-Mar-27	6,386	0	0	0	0%	0%
Valve Chamber		256	28-Jan-27	06-Mar-27	26,509	17,165	0	0	64.75%	0%
CO-PW-VC-290	Excavation Works for Main Line Valves and Valve Chambers of Potable Water Network for	80	28-Jan-27	08-Feb-27	1,657	1,657	0	0	100%	0%
CO-PW-VC-300	Installation Works for Valves of Potable Water Network for Alignment-RD-03-3	72	21-Feb-27	02-Mar-27	4,308	0	0	0	0%	0%
CO-PW-VC-310	Backfilling Works for Main Line Valves and Valve Chambers of Potable Water Network for	24	03-Mar-27	06-Mar-27	3,314	0	0	0	0%	0%
CO-PW-VC210	Installation of Valve Chambers of Potable Water Network for Alignment-RD-03-3	80	09-Feb-27	20-Feb-27	17,231	15,508	0	0	90%	0%
Fire Hydrant		176	09-Feb-27	06-Mar-27	8,994	506	0	0	5.63%	0%
CO-PW-FH-230	Excavation Works for Fire Hydrants of Potable Water Network for Alignment-RD-03-3	80	09-Feb-27	20-Feb-27	562	506	0	0	90%	0%
CO-PW-FH-240	Installation Works for Fire Hydrant of Potable Water Network for Alignment-RD-03-3	80	21-Feb-27	03-Mar-27	7,308	0	0	0	0%	0%
CO-PW-FH-250	Trench Backfilling and Compaction Works for Fire Hydrants of Potable Water Network for	16	04-Mar-27	06-Mar-27	1,124	0	0	0	0%	0%
Irrigation Network		176	09-Feb-27	06-Mar-27	89,958	2,077	0	0	2.31%	0%
Main Line Pipes		176	09-Feb-27	06-Mar-27	89,958	2,077	0	0	2.31%	0%
CO-IR-ML-350	Trench Excavation and Bedding Works for Main Lines of Irrigation Network for	80	09-Feb-27	20-Feb-27	2,307	2,077	0	0	90%	0%
CO-IR-ML-360	Pipes Laying Works for Main Lines of Irrigation Network for Alignment-RD-03-3	24	21-Feb-27	23-Feb-27	11,536	0	0	0	0%	0%
CO-IR-ML-370	Installation Works for Main Line Valves of Irrigation Network for Alignment-RD-03-3	24	24-Feb-27	27-Feb-27	5,680	0	0	0	0%	0%
CO-IR-ML-380	Trench Backfilling and Compaction Works for Main Lines of Irrigation Network for	24	03-Mar-27	06-Mar-27	4,615	0	0	0	0%	0%
CO-IR-ML-390	Installation Works for Bulbblers And Sprinkler and Irrigation Control System of Irrigation	24	28-Feb-27	02-Mar-27	65,819	0	0	0	0%	0%
Medium Voltage Network		96	16-Mar-27	29-Mar-27	2,657	0	0	0	0%	0%
Cabling Works		96	16-Mar-27	29-Mar-27	2,657	0	0	0	0%	0%
CO-MV-ML-340	Trench Excavation and Bedding Works for Medium Voltage Network for	24	16-Mar-27	18-Mar-27	617	0	0	0	0%	0%
CO-MV-ML-350	Duct Laying Works for Medium Voltage Network for Alignment-RD-03-3	24	23-Mar-27	25-Mar-27	1,402	0	0	0	0%	0%
CO-MV-ML-360	Trench Backfilling and Compaction Works for Medium Voltage Network for	24	27-Mar-27	29-Mar-27	637	0	0	0	0%	0%

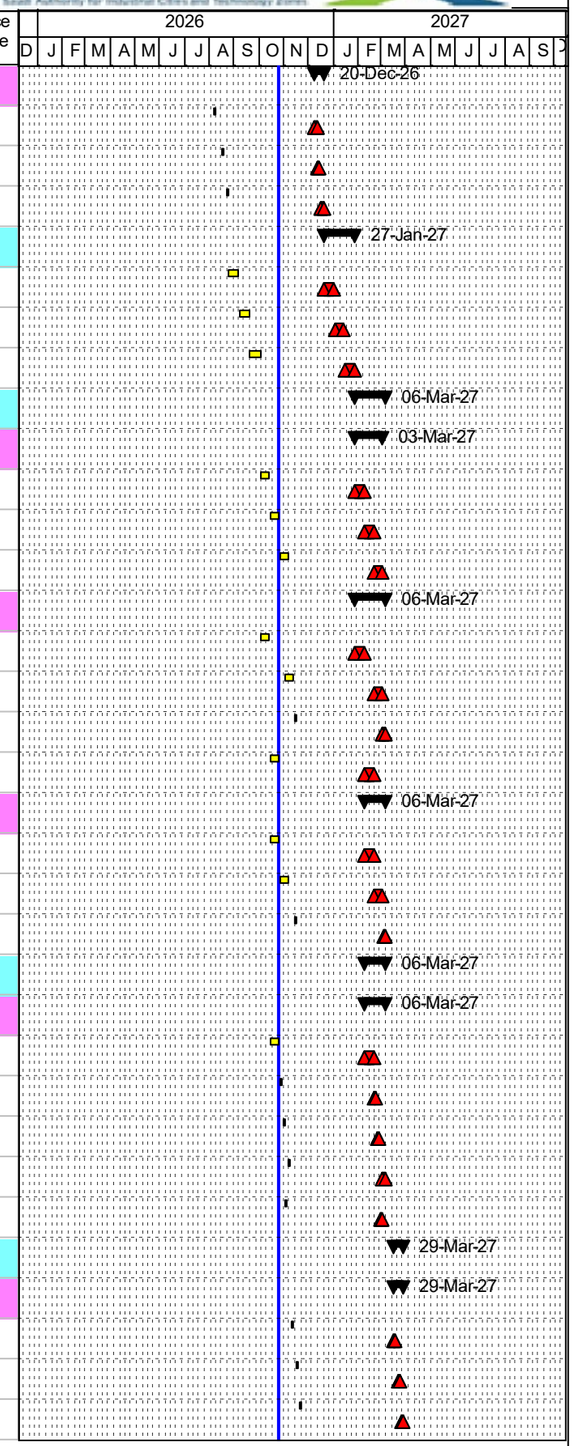


Primary Baseline
Remaining Work
Critical Remaining Work
Actual Work
Baseline Milestone
Milestone
Summary

Date	Revision	Checked	Approved
26-Oct-26	Third Industrial City		

Development of the Technology City in Dharan Project
BL-Update 26-10-2026
WPR UPS LEVEL 5


Activity ID	Activity Name	Original Duration	Start	Finish	Budgeted Total Cost	Planned Value Cost	Earned Value Cost	Actual Total Cost	Schedule % Complete	Performance % Complete
Low Voltage Network		224	30-Mar-27	01-May-27	40,657	0	0	0	0%	0%
Main Low Voltage Cables Works (Cable 300 MM)		144	30-Mar-27	19-Apr-27	21,013	0	0	0	0%	0%
CON-LV-ML-190	Trench Excavation and Bedding Works for Main Cable of Low Voltage Network for	56	30-Mar-27	06-Apr-27	4,104	0	0	0	0%	0%
CON-LV-ML-200	Cable Laying Works for Main Cable of Low Voltage Network for Alignment-RD-03-3	56	07-Apr-27	14-Apr-27	11,622	0	0	0	0%	0%
CON-LV-ML-210	Trench Backfilling and Compaction Works for Main Cable of Low Voltage Network for	32	15-Apr-27	19-Apr-27	5,287	0	0	0	0%	0%
Service Low Voltage Cables Works (Cable 70 MM)		136	07-Apr-27	26-Apr-27	18,960	0	0	0	0%	0%
CON-LV-HC-190	Trench Excavation and Bedding Works for Service Cable of Low Voltage Network for	56	07-Apr-27	14-Apr-27	2,051	0	0	0	0%	0%
CON-LV-HC-200	Cable Laying Works for Service Cable of Low Voltage Network for Alignment-RD-03-3	56	15-Apr-27	22-Apr-27	11,622	0	0	0	0%	0%
CON-LV-HC-210	Trench Backfilling and Compaction Works for Service Cable of Low Voltage Network for	24	24-Apr-27	26-Apr-27	5,287	0	0	0	0%	0%
Distribution Pillars Works		32	27-Apr-27	01-May-27	684	0	0	0	0%	0%
CON-LV-DP-190	Installation Works for Distribution Pillar Units of Low Voltage Network for Alignment-RD-03-3	32	27-Apr-27	01-May-27	684	0	0	0	0%	0%
Street Lighting Network		144	30-Mar-27	19-Apr-27	30,567	0	0	0	0%	0%
Lighting Poles Works		144	30-Mar-27	19-Apr-27	12,586	0	0	0	0%	0%
CO-SL-LP-450	Installation Works for Lighting Poles Foundation of Street Lighting Network for	48	30-Mar-27	05-Apr-27	2,697	0	0	0	0%	0%
CO-SL-LP-460	Installation Works for Lighting Poles of Street Lighting Network for Alignment-RD-03-3	48	06-Apr-27	12-Apr-27	8,990	0	0	0	0%	0%
CO-SL-LP-480	Backfilling Works for Lighting Poles of Street Lighting Network for Alignment-RD-03-3	48	13-Apr-27	19-Apr-27	899	0	0	0	0%	0%
Cabling Works		48	13-Apr-27	19-Apr-27	17,981	0	0	0	0%	0%
CO-SL-CL-350	Cable Laying Works for Street Lighting Network for Alignment-RD-03-3	48	13-Apr-27	19-Apr-27	9,889	0	0	0	0%	0%
CO-SL-CL-360	Trench Backfilling and Compaction Works for Street Lighting Network for Alignment-RD-03-3	48	13-Apr-27	19-Apr-27	8,091	0	0	0	0%	0%
Telecom and Light Current Network		208	08-Apr-27	08-May-27	232,186	0	0	0	0%	0%
Ducts Works		80	27-Apr-27	08-May-27	28,472	0	0	0	0%	0%
CO-TE-DW-230	Pipes Laying Works for Ducts of Telecom Network for Alignment-RD-03-3	48	27-Apr-27	03-May-27	19,575	0	0	0	0%	0%
CO-TE-DW-240	Trench Backfilling and Compaction Works for Ducts of Telecom Network for	32	04-May-27	08-May-27	8,898	0	0	0	0%	0%
Manholes Works		64	08-Apr-27	17-Apr-27	14,687	0	0	0	0%	0%
CO-TE-MH-230	Excavation Works for Manholes of Telecom Network for Alignment-RD-03-3	16	08-Apr-27	10-Apr-27	979	0	0	0	0%	0%
CO-TE-MH-240	Installation Works for Manholes of Telecom Network for Alignment-RD-03-3	24	11-Apr-27	13-Apr-27	10,770	0	0	0	0%	0%
CO-TE-MH-250	Backfilling Works for Manholes of Telecom Network for Alignment-RD-03-3	24	14-Apr-27	17-Apr-27	2,937	0	0	0	0%	0%
CCTV, Telephone, MSN, ACs System Works		24	18-Apr-27	20-Apr-27	189,027	0	0	0	0%	0%
CO-TE-CTV-210	Installation of CCTV, Telephone, ACS and MSN Systems Cables for Alignment-RD-03-3	24	18-Apr-27	20-Apr-27	189,027	0	0	0	0%	0%
Road Works		64	04-May-27	12-May-27	597,698	0	0	0	0%	0%
Pavement Works		32	04-May-27	08-May-27	585,170	0	0	0	0%	0%
CO-RD-PV-220	Fixing of Curbstone for Sidewalks Pavement for Alignment-RD-03-3	32	04-May-27	08-May-27	57,330	0	0	0	0%	0%
CO-RD-PV-230	Fixing of Interlock Tiles for Sidewalks Pavement for Alignment-RD-03-3	32	04-May-27	08-May-27	527,840	0	0	0	0%	0%
Traffic Signs Boards and Roads Marking		64	04-May-27	12-May-27	12,528	0	0	0	0%	0%

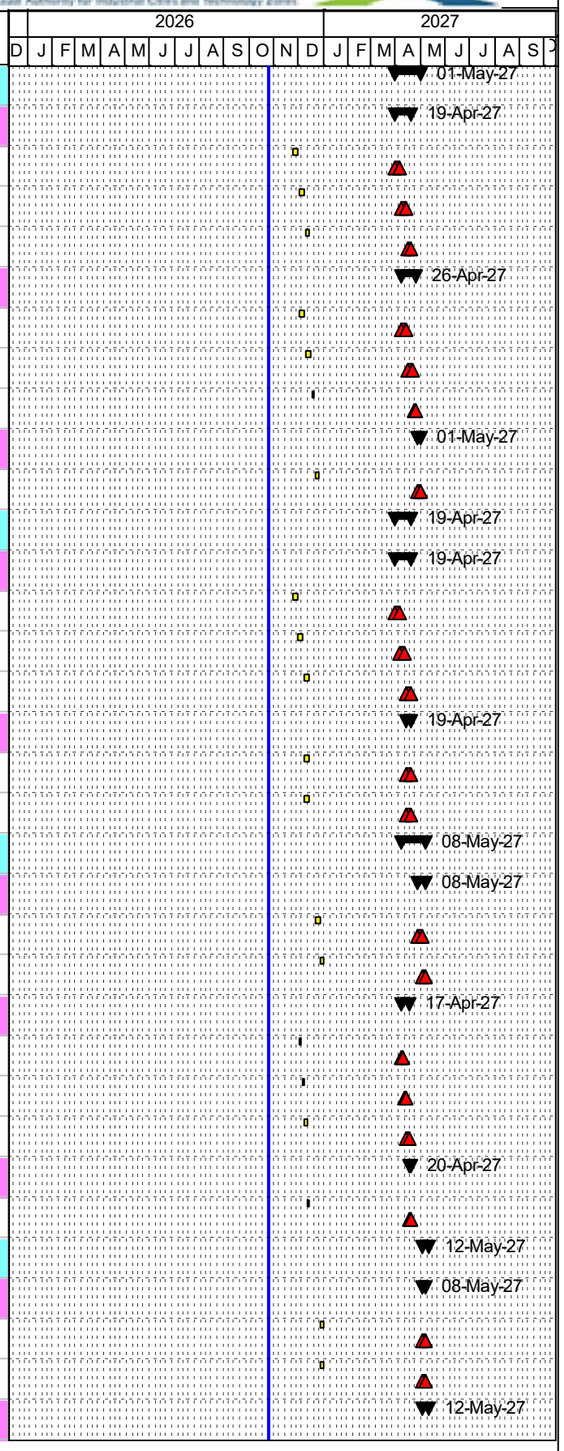

Primary Baseline | Actual Work | Summary
Remaining Work | Baseline Milestone
Critical Remaining Work | Milestone

Date	Revision	Checked	Approved
26-Oct-26	Third Industrial City		


Activity ID	Activity Name	Original Duration	Start	Finish	Budgeted Total Cost	Planned Value Cost	Earned Value Cost	Actual Total Cost	Schedule % Complete	Performance % Complete
CO-RD-F-RM-210	Application of Road Marking Works For Road Works for Alignment-RD-03-3	24	04-May-27	06-May-27	7,795	0	0	0	0%	0%
CO-RD-F-TS-150	Installation Works of Traffic Signs Boards For Road Works for Alignment-RD-03-3	32	09-May-27	12-May-27	4,734	0	0	0	0%	0%
Finishes for Infrastructure Networks		376	30-Mar-27	29-May-27	117,812	0	0	0	0%	0%
Storm Drainage Network		40	06-May-27	11-May-27	9,656	0	0	0	0%	0%
Testing and Finishes		40	06-May-27	11-May-27	9,656	0	0	0	0%	0%
CO-SD-ML-TF-130	Testing Work for Pipes of Storm Drainage Network for Alignment-RD-03-3	40	06-May-27	11-May-27	9,656	0	0	0	0%	0%
Potable Water Network		56	27-Apr-27	04-May-27	23,243	0	0	0	0%	0%
Testing and Finishes		56	27-Apr-27	04-May-27	23,243	0	0	0	0%	0%
CO-PW-TF-190	Testing of Potable Water Network for Alignment-RD-03-3	24	01-May-27	03-May-27	6,386	0	0	0	0%	0%
CO-PW-TF-200	Fire Hydrant Finishies (S.Box + Safety + Marker Post) of Potable Water Network for	24	27-Apr-27	29-Apr-27	2,249	0	0	0	0%	0%
CO-PW-TF-210	Final Finishes works and Covers for Valves and Valve Chambers for Alignment-RD-03-3	32	01-May-27	04-May-27	14,609	0	0	0	0%	0%
Treated Sewage Effluent (Tse)		48	23-May-27	29-May-27	1,510	0	0	0	0%	0%
Testing and Finishes		48	23-May-27	29-May-27	1,510	0	0	0	0%	0%
CO-TSE-TF-200	Final Testing (pressure tests) of Treated Sewage Effluent (Tse) for Alignment-RD-03-3	48	23-May-27	29-May-27	1,510	0	0	0	0%	0%
Irrigation Network		48	01-May-27	06-May-27	4,615	0	0	0	0%	0%
Testing and Finishes		48	01-May-27	06-May-27	4,615	0	0	0	0%	0%
CO-IR-TF-210	Final Testing (pressure tests) of Irrigation Network for Alignment-RD-03-3	48	01-May-27	06-May-27	4,615	0	0	0	0%	0%
Medium Voltage Network		48	30-Mar-27	05-Apr-27	510	0	0	0	0%	0%
Termination and Testing Works		48	30-Mar-27	05-Apr-27	510	0	0	0	0%	0%
CO-MV-TF-250	Testing and Termination Works of Medium Voltage Network for Alignment-RD-03-3	48	30-Mar-27	05-Apr-27	510	0	0	0	0%	0%
Low Voltage Network		48	02-May-27	08-May-27	8,454	0	0	0	0%	0%
Termination and Testing Works		48	02-May-27	08-May-27	8,454	0	0	0	0%	0%
CON-LV-TT-160	Testing and Termination Works for Substation Low Voltage Panel Boards of Low Voltage	48	02-May-27	08-May-27	8,454	0	0	0	0%	0%
Street Lighting Network		136	27-Apr-27	22-May-27	12,457	0	0	0	0%	0%
Termination and Testing Works		136	27-Apr-27	22-May-27	11,254	0	0	0	0%	0%
CO-SL-LP-470	Installation Works for Lighting Fixtures With Drop Wire of Street Lighting Network for	48	27-Apr-27	03-May-27	5,860	0	0	0	0%	0%
CO-SL-TF-490	Testing Works for Lighting Poles of Street Lighting Network for Alignment-RD-03-3	48	10-May-27	22-May-27	5,394	0	0	0	0%	0%
Earthing System Works		88	27-Apr-27	09-May-27	1,203	0	0	0	0%	0%
CO-SL-ES-280	Install Earthing System Works for Lighting Poles of Street Lighting Network for	48	27-Apr-27	03-May-27	601	0	0	0	0%	0%
CO-SL-ES-290	Install Earthing System Works for Lighting Panel Boards of Street Lighting Network for	48	03-May-27	09-May-27	601	0	0	0	0%	0%
Telecom and Light Current Network		96	22-Apr-27	05-May-27	57,368	0	0	0	0%	0%
Testing and Finishes		96	22-Apr-27	05-May-27	57,368	0	0	0	0%	0%
CO-TE-CTV-TF-260	Testing and Interface modules with Telecom for Alignment-RD-03-3	48	22-Apr-27	28-Apr-27	12,014	0	0	0	0%	0%
CO-TE-CTV-TF-340	Testing and Interface modules with CCTV, Telephone, MSN and Access Control for	48	29-Apr-27	05-May-27	45,355	0	0	0	0%	0%

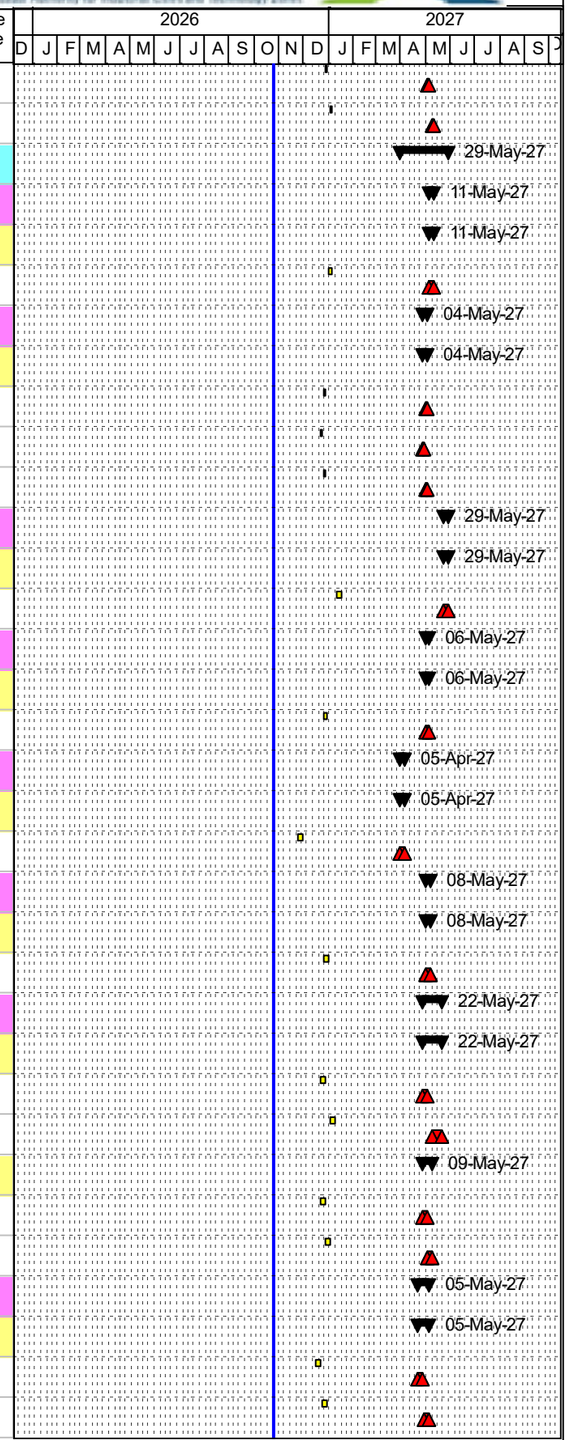

Primary Baseline | Actual Work | Summary
Remaining Work | Baseline Milestone
Critical Remaining Work | Milestone

Date	Revision	Checked	Approved
26-Oct-26	Third Industrial City		


Activity ID	Activity Name	Original Duration	Start	Finish	Budgeted Total Cost	Planned Value Cost	Earned Value Cost	Actual Total Cost	Schedule % Complete	Performance % Complete
External		2720	01-Apr-26 A	11-May-27	25,187,577	15,653,735	10,624,269	10,346,026	62.15%	42.18%
External Road - 1 - 1		2712	01-Apr-26 A	10-May-27	5,221,714	3,247,135	2,608,226	2,608,226	62.19%	49.95%
Earthworks		1824	01-Apr-26 A	28-Dec-26	3,247,135	3,247,135	2,608,226	2,608,226	100%	80.32%
Earthworks		1824	01-Apr-26 A	28-Dec-26	3,247,135	3,247,135	2,608,226	2,608,226	100%	80.32%
CO-EW-250	Excavation and Backfilling Works Upto Design Level for Earthworks for External Road - 1 -	536	01-Apr-26 A	22-Jun-26 A	2,608,226	2,608,226	2,608,226	2,608,226	100%	100%
CO-EW-250_R	Excavation and Backfilling Works Upto Design Level for Earthworks for External Road - 1 -	64	20-Dec-26	28-Dec-26	638,908	638,908	0	0	100%	0%
Road Works		304	28-Mar-27	10-May-27	1,974,580	0	0	0	0%	0%
Road 01		304	28-Mar-27	10-May-27	1,974,580	0	0	0	0%	0%
Pre-Bituminous Construction		136	28-Mar-27	15-Apr-27	532,798	0	0	0	0%	0%
CO-RD-PB-240	Subgrade Layer for Road Works for External Road - 1 - 1	64	28-Mar-27	05-Apr-27	259,905	0	0	0	0%	0%
CO-RD-PB-250	Aggregate Base Course Layer for Road Works for External Road - 1 - 1	72	06-Apr-27	15-Apr-27	272,894	0	0	0	0%	0%
Bituminous Construction		64	17-Apr-27	25-Apr-27	1,102,685	0	0	0	0%	0%
CO-RD-B-260	Bituminous Base Courses Layers for Road Works for External Road - 1 - 1	32	17-Apr-27	20-Apr-27	548,740	0	0	0	0%	0%
CON-RD-MR-250	Preparation of Asphaltic Wearing Course Layer for Roads Network for External Road - 1	32	21-Apr-27	25-Apr-27	553,945	0	0	0	0%	0%
Pavement Works		112	21-Apr-27	06-May-27	301,042	0	0	0	0%	0%
CO-RD-PV-260	Fixing of Curbstone for Sidewalks Pavement for External Road - 1 - 1	64	21-Apr-27	29-Apr-27	183,454	0	0	0	0%	0%
CO-RD-PV-270	Fixing of Interlock Tiles for Sidewalks Pavement for External Road - 1 - 1	48	01-May-27	06-May-27	117,588	0	0	0	0%	0%
Traffic Signs Boards and Roads Marking		24	08-May-27	10-May-27	38,054	0	0	0	0%	0%
CO-RD-F-RM-230	Application of Road Marking Works For Road Works for External Road - 1 - 1	16	08-May-27	09-May-27	24,799	0	0	0	0%	0%
CO-RD-F-TS-170	Installation Works of Traffic Signs Boards For Road Works for External Road - 1 - 1	8	10-May-27	10-May-27	13,255	0	0	0	0%	0%
External Road - 1 - 2		2608	18-Apr-26 A	11-May-27	7,651,591	4,767,067	1,790,191	1,214,285	62.3%	23.4%
Earthworks		1560	18-Apr-26 A	18-Jan-27	4,767,067	4,767,067	1,790,191	1,214,285	100%	37.55%
Earthworks		1560	18-Apr-26 A	18-Jan-27	4,767,067	4,767,067	1,790,191	1,214,285	100%	37.55%
CO-EW-280	Excavation and Backfilling Works Upto Design Level for Earthworks for External Road - 1 -	424	18-Apr-26 A	22-Jun-26 A	622,155	622,155	622,155	622,155	100%	100%
CO-EW-280_R	Excavation and Backfilling Works Upto Design Level for Earthworks for External Road - 1 -	168	26-Sep-26 A	18-Jan-27	4,144,912	4,144,912	1,168,036	592,130	100%	28.18%
Road Works		312	28-Mar-27	11-May-27	2,884,524	0	0	0	0%	0%
Road 01		312	28-Mar-27	11-May-27	2,884,524	0	0	0	0%	0%
Pre-Bituminous Construction		96	28-Mar-27	10-Apr-27	778,172	0	0	0	0%	0%
CO-RD-PB-300	Subgrade Layer for Road Works for External Road - 1 - 2	48	28-Mar-27	03-Apr-27	379,600	0	0	0	0%	0%
CO-RD-PB-310	Aggregate Base Course Layer for Road Works for External Road - 1 - 2	48	04-Apr-27	10-Apr-27	398,572	0	0	0	0%	0%
Bituminous Construction		88	11-Apr-27	22-Apr-27	1,610,525	0	0	0	0%	0%
CO-RD-B-320	Bituminous Base Courses Layers for Road Works for External Road - 1 - 2	56	11-Apr-27	18-Apr-27	801,462	0	0	0	0%	0%
CON-RD-MR-310	Preparation of Asphaltic Wearing Course Layer for Roads Network for External Road - 1	32	19-Apr-27	22-Apr-27	809,064	0	0	0	0%	0%
Pavement Works		96	20-Apr-27	03-May-27	439,683	0	0	0	0%	0%

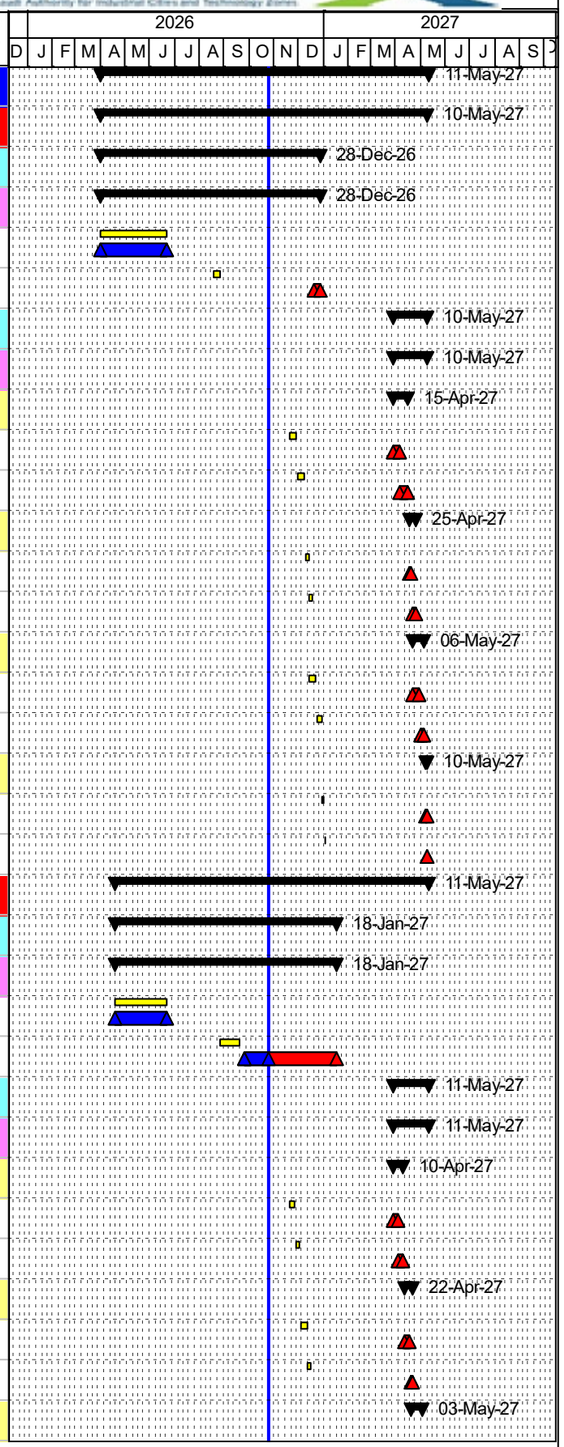

Primary Baseline | Actual Work | Summary
Remaining Work | Baseline Milestone
Critical Remaining Work | Milestone

Date	Revision	Checked	Approved
26-Oct-26	Third Industrial City		

Activity ID	Activity Name	Original Duration	Start	Finish	Budgeted Total Cost	Planned Value Cost	Earned Value Cost	Actual Total Cost	Schedule % Complete	Performance % Complete
CO-RD-PV-320	Fixing of Curbstone for Sidewalks Pavement for External Road - 1 - 2	48	20-Apr-27	26-Apr-27	267,941	0	0	0	0%	0%
CO-RD-PV-330	Fixing of Interlock Tiles for Sidewalks Pavement for External Road - 1 - 2	48	27-Apr-27	03-May-27	171,741	0	0	0	0%	0%
Traffic Signs Boards and Roads Marking		56	04-May-27	11-May-27	56,143	0	0	0	0%	0%
CO-RD-F-RM-260	Application of Road Marking Works For Road Works for External Road - 1 - 2	32	04-May-27	08-May-27	36,261	0	0	0	0%	0%
CO-RD-F-TS-200	Installation Works of Traffic Signs Boards For Road Works for External Road - 1 - 2	24	09-May-27	11-May-27	19,882	0	0	0	0%	0%
External Road - 2		2464	09-May-26 A	11-May-27	3,781,297	2,348,995	1,330,763	1,330,763	62.12%	35.19%
Earthworks		1880	09-May-26 A	11-Feb-27	2,348,995	2,348,995	1,330,763	1,330,763	100%	56.65%
Earthworks		1880	09-May-26 A	11-Feb-27	2,348,995	2,348,995	1,330,763	1,330,763	100%	56.65%
CO-EW-260	Excavation and Backfilling Works Upto Design Level for Earthworks for External Road -	280	09-May-26 A	22-Jun-26 A	1,330,763	1,330,763	1,330,763	1,330,763	100%	100%
CO-EW-260_R	Excavation and Backfilling Works Upto Design Level for Earthworks for External Road -	168	19-Jan-27	11-Feb-27	1,018,232	1,018,232	0	0	100%	0%
Road Works		360	21-Mar-27	11-May-27	1,432,302	0	0	0	0%	0%
Road 01		360	21-Mar-27	11-May-27	1,432,302	0	0	0	0%	0%
Pre-Bituminous Construction		56	21-Mar-27	28-Mar-27	386,518	0	0	0	0%	0%
CO-RD-PB-260	Subgrade Layer for Road Works for External Road - 2	56	21-Mar-27	28-Mar-27	188,547	0	0	0	0%	0%
CO-RD-PB-270	Aggregate Base Course Layer for Road Works for External Road - 2	32	24-Mar-27	28-Mar-27	197,971	0	0	0	0%	0%
Bituminous Construction		160	29-Mar-27	20-Apr-27	799,946	0	0	0	0%	0%
CO-RD-B-280	Bituminous Base Courses Layers for Road Works for External Road - 2	80	29-Mar-27	08-Apr-27	398,085	0	0	0	0%	0%
CON-RD-MR-270	Preparation of Asphaltic Wearing Course Layer for Roads Network for External Road - 2	80	10-Apr-27	20-Apr-27	401,861	0	0	0	0%	0%
Pavement Works		72	20-Apr-27	29-Apr-27	218,390	0	0	0	0%	0%
CO-RD-PV-280	Fixing of Curbstone for Sidewalks Pavement for External Road - 2	72	20-Apr-27	29-Apr-27	133,086	0	0	0	0%	0%
CO-RD-PV-290	Fixing of Interlock Tiles for Sidewalks Pavement for External Road - 2	72	20-Apr-27	29-Apr-27	85,304	0	0	0	0%	0%
Traffic Signs Boards and Roads Marking		80	01-May-27	11-May-27	27,448	0	0	0	0%	0%
CO-RD-F-RM-240	Application of Road Marking Works For Road Works for External Road - 2	80	01-May-27	11-May-27	17,980	0	0	0	0%	0%
CO-RD-F-TS-180	Installation Works of Traffic Signs Boards For Road Works for External Road - 2	16	03-May-27	04-May-27	9,468	0	0	0	0%	0%
External Road - 3		2464	09-May-26 A	11-May-27	8,532,974	5,290,538	4,895,089	5,192,752	62%	57.37%
Earthworks		1752	09-May-26 A	20-Feb-27	5,285,229	5,285,229	4,540,017	4,837,557	100%	85.9%
Earthworks		1752	09-May-26 A	20-Feb-27	5,285,229	5,285,229	4,540,017	4,837,557	100%	85.9%
CO-EW-270	Excavation and Backfilling Works Upto Design Level for Earthworks for External Road -	280	09-May-26 A	22-Jun-26 A	2,968,746	2,968,746	2,968,746	2,968,746	100%	100%
CO-EW-270_R	Excavation and Backfilling Works Upto Design Level for Earthworks for External Road -	168	23-Aug-26 A	20-Feb-27	2,316,484	2,316,484	1,571,271	1,868,812	38.1%	67.83%
Telecom and Light Current Network		344	02-Feb-27	27-Mar-27	38,794	5,309	0	0	13.68%	0%
Manholes Works		296	02-Feb-27	20-Mar-27	29,095	5,309	0	0	18.25%	0%
CO-TE-MH-290	Excavation Works for Manholes of Telecom Network for External Road - 3	144	02-Feb-27	22-Feb-27	1,940	1,940	0	0	100%	0%
CO-TE-MH-300	Installation Works for Manholes of Telecom Network for External Road - 3	152	23-Feb-27	20-Mar-27	21,337	3,369	0	0	15.79%	0%
CO-TE-MH-310	Backfilling Works for Manholes of Telecom Network for External Road - 3	48	14-Mar-27	20-Mar-27	5,819	0	0	0	0%	0%

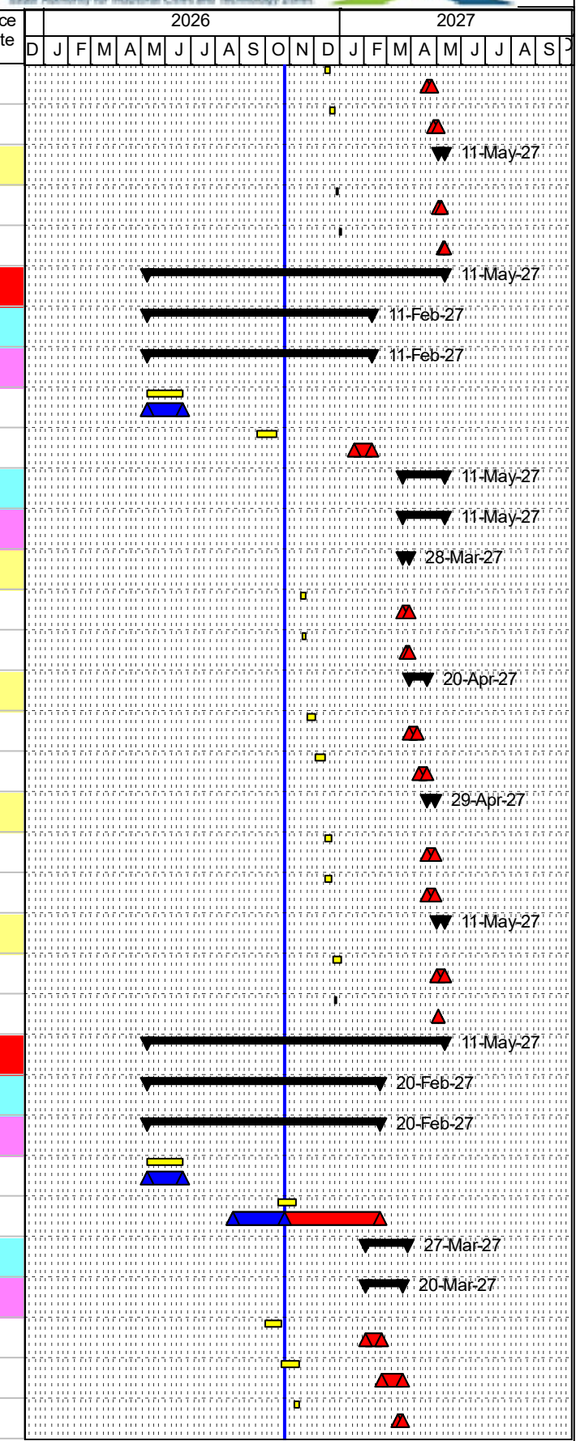


Primary Baseline | Actual Work | Summary
Remaining Work | Baseline Milestone
Critical Remaining Work | Milestone

Date	Revision	Checked	Approved
26-Oct-26	Third Industrial City		

Development of the Technology City in Dharan Project
BL-Update 26-10-2026
WPR UPS LEVEL 5

Activity ID	Activity Name	Original Duration	Start	Finish	Budgeted Total Cost	Planned Value Cost	Earned Value Cost	Actual Total Cost	Schedule % Complete	Performance % Complete
Testing and Finishes		48	21-Mar-27	27-Mar-27	9,698	0	0	0	0%	0%
CO-TE-CTV-TF-360	Testing and Interface modules with Telecom for External Road - 3	48	21-Mar-27	27-Mar-27	9,698	0	0	0	0%	0%
Road Works		688	08-Sep-26 A	11-May-27	3,208,951	0	355,073	355,195	0%	11.07%
Road 01		688	08-Sep-26 A	11-May-27	3,208,951	0	355,073	355,195	0%	11.07%
Pre-Bituminous Construction		440	08-Sep-26 A	05-Apr-27	865,798	0	355,073	355,195	0%	41.01%
CO-RD-PB-280	Subgrade Layer for Road Works for External Road - 3	48	08-Sep-26 A	27-Mar-27	422,344	0	211,172	211,178	0%	50%
CO-RD-PB-290	Aggregate Base Course Layer for Road Works for External Road - 3	88	19-Oct-26 A	05-Apr-27	443,453	0	143,901	144,017	0%	32.45%
Bituminous Construction		184	10-Apr-27	05-May-27	1,791,868	0	0	0	0%	0%
CO-RD-B-300	Bituminous Base Courses Layers for Road Works for External Road - 3	96	10-Apr-27	22-Apr-27	891,705	0	0	0	0%	0%
CON-RD-MR-290	Preparation of Asphaltic Wearing Course Layer for Roads Network for External Road - 3	88	24-Apr-27	05-May-27	900,163	0	0	0	0%	0%
Pavement Works		24	01-May-27	03-May-27	489,192	0	0	0	0%	0%
CO-RD-PV-300	Fixing of Curbstone for Sidewalks Pavement for External Road - 3	24	01-May-27	03-May-27	298,112	0	0	0	0%	0%
CO-RD-PV-310	Fixing of Interlock Tiles for Sidewalks Pavement for External Road - 3	24	01-May-27	03-May-27	191,080	0	0	0	0%	0%
Traffic Signs Boards and Roads Marking		40	06-May-27	11-May-27	62,093	0	0	0	0%	0%
CO-RD-F-RM-250	Application of Road Marking Works For Road Works for External Road - 3	40	06-May-27	11-May-27	40,318	0	0	0	0%	0%
CO-RD-F-TS-190	Installation Works of Traffic Signs Boards For Road Works for External Road - 3	24	06-May-27	09-May-27	21,775	0	0	0	0%	0%
Superstructure Work		1808	01-Aug-26 A	23-Jun-27	35,692,170	3,020,557	9,670,095	9,311,610	8.46%	27.09%
Utility Buildings		1808	29-Aug-26 A	23-Jun-27	8,083,982	1,059,788	1,082,796	1,061,039	13.11%	13.39%
Water Pump Station		1808	15-Sep-26 A	23-Jun-27	3,313,461	580,935	346,091	346,091	17.53%	10.45%
Civil work		568	15-Sep-26 A	15-Dec-26	445,078	445,078	346,091	346,091	100%	77.76%
SubStructure		360	15-Sep-26 A	15-Nov-26	318,456	318,456	314,735	314,735	100%	98.83%
CO-UB-PS-100	Excavation Work for Water Pump station building	64	15-Sep-26 A	17-Sep-26 A	3,721	3,721	3,721	3,721	100%	100%
CO-UB-PS-110	pouring P.C Conceret for Water Pump station building	16	19-Sep-26 A	20-Sep-26 A	296,132	296,132	296,132	296,132	100%	100%
CO-UB-PS-120	Formwork for Foundation for Water Pump station building	56	26-Sep-26 A	27-Sep-26 A	3,721	3,721	3,721	3,721	100%	100%
CO-UB-PS-130	Steel fixing for Foundation for Water Pump station building	48	27-Sep-26 A	28-Sep-26 A	3,721	3,721	3,721	3,721	100%	100%
CO-UB-PS-140	pouring for Foundation for Water Pump station building	8	01-Oct-26 A	03-Oct-26 A	3,721	3,721	3,721	3,721	100%	100%
CO-UB-PS-150	curing and deshuttering formwork Pump station building	56	06-Oct-26 A	10-Oct-26 A	3,721	3,721	3,721	3,721	100%	100%
CO-UB-PS-160	Backfilling and compaction work for pump station	32	11-Nov-26	15-Nov-26	3,721	3,721	0	0	100%	0%
Super structure		240	06-Oct-26 A	15-Dec-26	126,623	126,623	31,356	31,356	100%	24.76%
CO-UB-PS-170	Formwork for Wall and columns for Water Pump station building	40	06-Oct-26 A	08-Oct-26 A	10,452	10,452	10,452	10,452	100%	100%
CO-UB-PS-180	Steel fixing for Wall columns	32	08-Oct-26 A	10-Oct-26 A	10,452	10,452	10,452	10,452	100%	100%
CO-UB-PS-190	pouring for Wall columns	8	11-Oct-26 A	12-Oct-26 A	10,452	10,452	10,452	10,452	100%	100%
CO-UB-PS-200	curing and deshuttering formwork for Wall columns	56	16-Nov-26	23-Nov-26	10,452	10,452	0	0	100%	0%
CO-UB-PS-210	Waterproofing for Walls columns	16	24-Nov-26	25-Nov-26	10,452	10,452	0	0	100%	0%

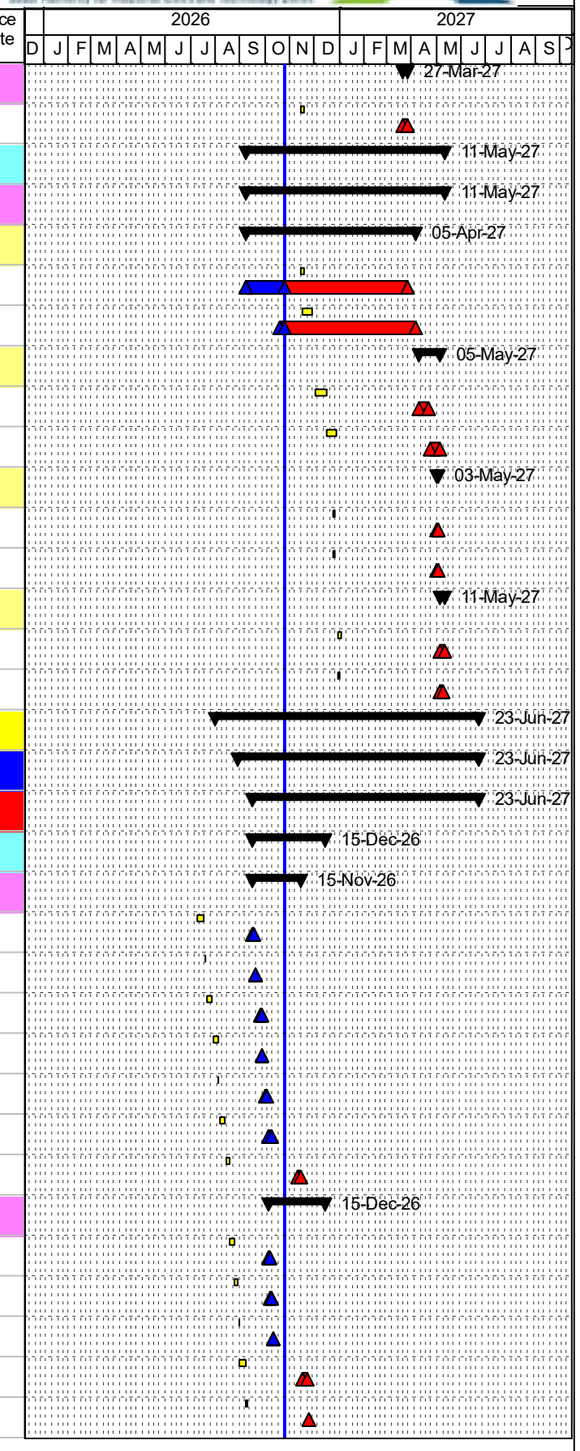


Primary Baseline | Actual Work | Summary
Remaining Work | Baseline Milestone
Critical Remaining Work | Milestone

Date	Revision	Checked	Approved
26-Oct-26	Third Industrial City		

Development of the Technology City in Dharan Project
BL-Update 26-10-2026
WPR UPS LEVEL 5

Activity ID	Activity Name	Original Duration	Start	Finish	Budgeted Total Cost	Planned Value Cost	Earned Value Cost	Actual Total Cost	Schedule % Complete	Performance % Complete
CO-UB-PS-220	Formwork for pump roof	32	26-Nov-26	30-Nov-26	17,183	17,183	0	0	100%	0%
CO-UB-PS-230	Steel fixing for pump roof	32	01-Dec-26	05-Dec-26	17,183	17,183	0	0	100%	0%
CO-UB-PS-240	pouring for pump roof	16	06-Dec-26	07-Dec-26	17,183	17,183	0	0	100%	0%
CO-UB-PS-250	curing and deshuttering formwork for pump roof	56	08-Dec-26	15-Dec-26	22,812	22,812	0	0	100%	0%
Architectural work		240	16-Dec-26	19-Jan-27	152,986	135,856	0	0	88.8%	0%
CO-UB-PS-260	Executing Masonry Works for Water Pump station building	56	16-Dec-26	23-Dec-26	44,161	44,161	0	0	100%	0%
CO-UB-PS-270	Executing Plastering Works for Pump station building	56	24-Dec-26	31-Dec-26	43,051	43,051	0	0	100%	0%
CO-UB-PS-280	Executing Painting and Finishes Works for Pump station building	64	02-Jan-27	10-Jan-27	55,593	48,644	0	0	87.5%	0%
CO-UB-PS-320	Doors and windows Fixing &Stair Tiles	64	11-Jan-27	19-Jan-27	10,180	0	0	0	0%	0%
Mechanical work		288	08-May-27	23-Jun-27	2,715,397	0	0	0	0%	0%
CO-UB-PS-340	Executing HVAC System for Water Pump station building	80	08-May-27	24-May-27	88,142	0	0	0	0%	0%
CO-UB-PS-360	Executing Fire fighting institution works(piping and wire installation) for Water Pump station	80	25-May-27	05-Jun-27	19,869	0	0	0	0%	0%
CO-UB-PS-380	Executing Plummbing works for Water Pump station building	80	06-Jun-27	16-Jun-27	524,160	0	0	0	0%	0%
CO-UB-PS-390	Installation of pumps	48	17-Jun-27	23-Jun-27	2,083,226	0	0	0	0%	0%
Sewage Lift Station		480	29-Aug-26 A	28-Jan-27	564,483	0	372,559	350,805	0%	66%
Civil work		480	29-Aug-26 A	25-Jan-27	416,344	0	372,559	350,805	0%	89.48%
Sup Structure		384	29-Aug-26 A	10-Oct-26 A	228,618	0	228,618	228,618	0%	100%
CO-UB-LS-220	Excavation Work for Sewage Lift Station	72	29-Aug-26 A	31-Aug-26 A	34,665	0	34,665	34,665	0%	100%
CO-UB-LS-230	pouring P.C Conceret for Sewage Lift Station	16	01-Sep-26 A	02-Sep-26 A	20,627	0	20,627	20,627	0%	100%
CO-UB-LS-240	Formwork for Foundation for Sewage Lift Station	96	03-Sep-26 A	03-Oct-26 A	34,665	0	34,665	34,665	0%	100%
CO-UB-LS-250	Steel fixing for Foundation for Sewage Lift Station	80	03-Sep-26 A	06-Oct-26 A	34,665	0	34,665	34,665	0%	100%
CO-UB-LS-260	pouring for Foundationfor Sewage Lift Station	16	03-Sep-26 A	08-Oct-26 A	34,665	0	34,665	34,665	0%	100%
CO-UB-LS-270	curing and deshuttering formwork for Sewage Lift Station	56	03-Sep-26 A	10-Oct-26 A	34,665	0	34,665	34,665	0%	100%
CO-UB-LS-280	Backfilling and compaction work for Sewage Lift Station	48	03-Sep-26 A	10-Oct-26 A	34,665	0	34,665	34,665	0%	100%
Super structure		352	30-Sep-26 A	25-Jan-27	187,726	0	143,941	122,187	0%	76.68%
CO-UB-LS-290	Formwork for Wall and columns for Sewage Lift Station	80	30-Sep-26 A	04-Oct-26 A	14,769	0	14,769	14,769	0%	100%
CO-UB-LS-300	Steel fixing for Wall columns	72	05-Oct-26 A	06-Oct-26 A	14,769	0	14,769	14,769	0%	100%
CO-UB-LS-310	pouring for Wall columns	8	07-Oct-26 A	08-Oct-26 A	14,769	0	14,769	14,769	0%	100%
CO-UB-LS-320	curing and deshuttering formwork for Wall columns	56	11-Oct-26 A	12-Oct-26 A	14,769	0	14,769	14,769	0%	100%
CO-UB-LS-330	Waterproofing for Walls columns	32	12-Oct-26 A	13-Oct-26 A	14,769	0	14,769	14,769	0%	100%
CO-UB-LS-340	Formwork for pump roof	48	13-Oct-26 A	15-Oct-26 A	24,170	0	24,170	24,170	0%	100%
CO-UB-LS-350	Steel fixing for pump roof	48	17-Oct-26 A	18-Oct-26 A	24,170	0	24,170	24,170	0%	100%
CO-UB-LS-360	pouring for pump roof	8	18-Oct-26 A	11-Jan-27	24,170	0	21,753	0	0%	90%
CO-UB-LS-370	curing and deshuttering formwork for pump roof	96	12-Jan-27	25-Jan-27	41,368	0	0	0	0%	0%

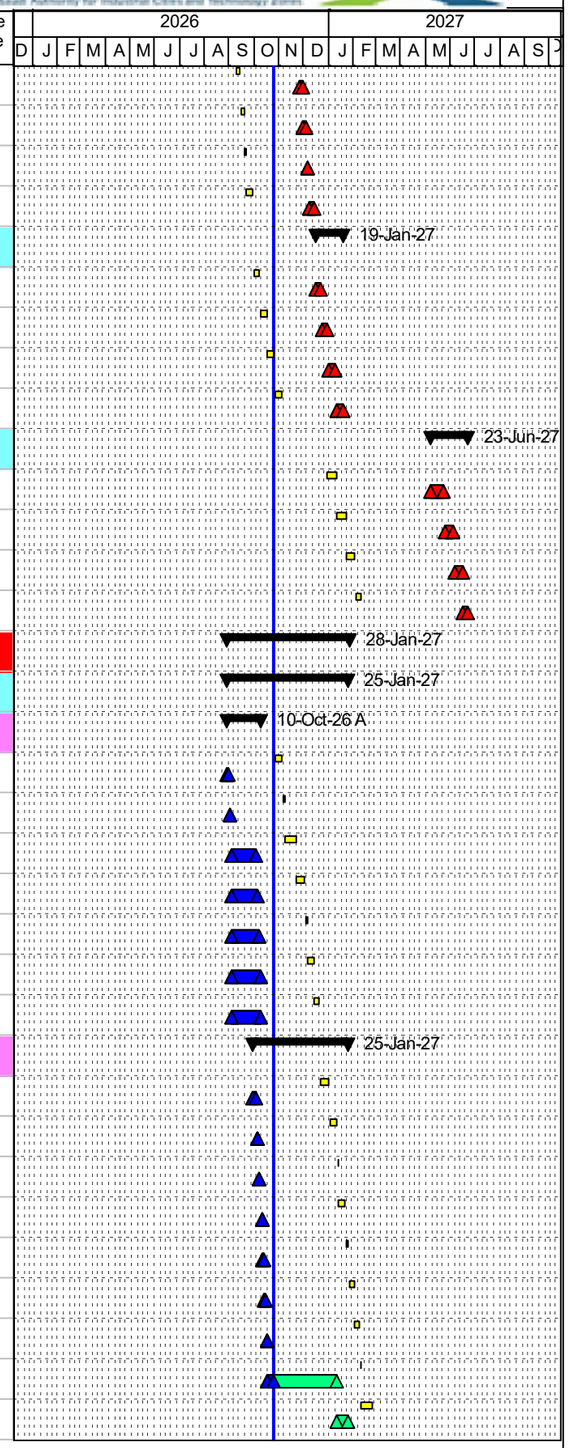


Primary Baseline | Actual Work | Summary
Remaining Work | Baseline Milestone
Critical Remaining Work | Milestone

Date	Revision	Checked	Approved
26-Oct-26	Third Industrial City		

Development of the Technology City in Dharan Project
BL-Update 26-10-2026
WPR UPS LEVEL 5


Activity ID	Activity Name	Original Duration	Start	Finish	Budgeted Total Cost	Planned Value Cost	Earned Value Cost	Actual Total Cost	Schedule % Complete	Performance % Complete
Architectural work		24	26-Jan-27	28-Jan-27	148,139	0	0	0	0%	0%
CO-UB-LS-390	Executing Plastering and Finishes Works for Sewage Lift Station	24	26-Jan-27	28-Jan-27	148,139	0	0	0	0%	0%
Potable Water Tank		616	02-Jan-27	04-Apr-27	314,972	29,027	0	0	9.22%	0%
Eearth Work		176	02-Jan-27	26-Jan-27	99,522	29,027	0	0	29.17%	0%
CO-UB-PWT-100	Excavation work for tank foundation tank formation level for Potable Water Tank	96	02-Jan-27	14-Jan-27	49,761	29,027	0	0	58.33%	0%
CO-UB-PWT-110	Soil replacement Up to tank formation level for Potable Water Tank	80	16-Jan-27	26-Jan-27	49,761	0	0	0	0%	0%
Structural Work		328	27-Jan-27	18-Mar-27	168,191	0	0	0	0%	0%
CO-UB-PWT-120	Plain Concrete works for Potable Water Tank	56	27-Jan-27	03-Feb-27	18,908	0	0	0	0%	0%
CO-UB-PWT-130	Form work for Tank Foundation for Potable Water Tank	96	04-Feb-27	17-Feb-27	49,761	0	0	0	0%	0%
CO-UB-PWT-140	Steel Reinforcement work for Tank Foundation for Potable Water Tank	96	18-Feb-27	03-Mar-27	49,761	0	0	0	0%	0%
CO-UB-PWT-150	Casting concrete for Tank Foundation for Potable Water Tank	80	04-Mar-27	18-Mar-27	49,761	0	0	0	0%	0%
Tank Shell Erection&Roof Installation		112	20-Mar-27	04-Apr-27	47,259	0	0	0	0%	0%
CO-UB-PWT-170	shell erection for Potable Water Tank	112	20-Mar-27	04-Apr-27	47,259	0	0	0	0%	0%
IrrigationTank		512	16-Jan-27	03-Apr-27	314,972	0	0	0	0%	0%
Eearth Work		176	16-Jan-27	09-Feb-27	99,522	0	0	0	0%	0%
CO-UB-IRT-140	Excavation work for tank foundation tank formation level for Irrigation Tank	96	16-Jan-27	28-Jan-27	49,761	0	0	0	0%	0%
CO-UB-IRT-150	Soil replacement Up to tank formation level for Irrigation Tank	80	30-Jan-27	09-Feb-27	49,761	0	0	0	0%	0%
Structural Work		224	10-Feb-27	17-Mar-27	168,191	0	0	0	0%	0%
CO-UB-IRT-160	Plain Concrete works for Irrigation Tank	24	10-Feb-27	13-Feb-27	18,908	0	0	0	0%	0%
CO-UB-IRT-170	Form work for Tank Foundation for Irrigation Tank	80	14-Feb-27	24-Feb-27	49,761	0	0	0	0%	0%
CO-UB-IRT-180	Steel Reinforcement work for Tank Foundation for Irrigation Tank	88	25-Feb-27	13-Mar-27	49,761	0	0	0	0%	0%
CO-UB-IRT-190	Casting concrete for Tank Foundation for Irrigation Tank	32	14-Mar-27	17-Mar-27	49,761	0	0	0	0%	0%
Tank Shell Erection&Roof Installation		112	18-Mar-27	03-Apr-27	47,259	0	0	0	0%	0%
CO-UB-IRT-210	shell erection for Irrigation Tank	112	18-Mar-27	03-Apr-27	47,259	0	0	0	0%	0%
Control Room		1024	03-Oct-26 A	13-May-27	3,576,093	449,827	364,146	364,142	12.58%	10.18%
Civil Work		272	03-Oct-26 A	06-Jan-27	472,675	449,827	364,146	364,142	95.17%	77.04%
CO-UB-CR-100	Excavation Work For Control Room Foundation	56	03-Oct-26 A	04-Oct-26 A	7,427	7,427	7,427	7,427	100%	100%
CO-UB-CR-110	Pouring for Plain Concrete	40	05-Oct-26 A	11-Oct-26 A	265,188	265,188	265,188	265,188	100%	100%
CO-UB-CR-120	Pouring R.C Footing For Control Room	168	13-Oct-26 A	17-Oct-26 A	7,427	7,427	7,427	7,427	100%	100%
CO-UB-CR-130	Pouring R.C Columns For Control Room	96	19-Oct-26 A	24-Oct-26 A	78,391	78,391	78,391	78,391	100%	100%
CO-UB-CR-140	Pouring Beams and Slab For Control Room	80	25-Oct-26 A	06-Jan-27	114,241	91,393	5,712	5,709	80%	5%
Finishing Work		760	20-Jan-27	13-May-27	3,103,418	0	0	0	0%	0%
Architictural work		336	20-Jan-27	13-Mar-27	362,218	0	0	0	0%	0%
CO-UB-CR-150	Brick Work For Control Room	80	20-Jan-27	31-Jan-27	99,292	0	0	0	0%	0%

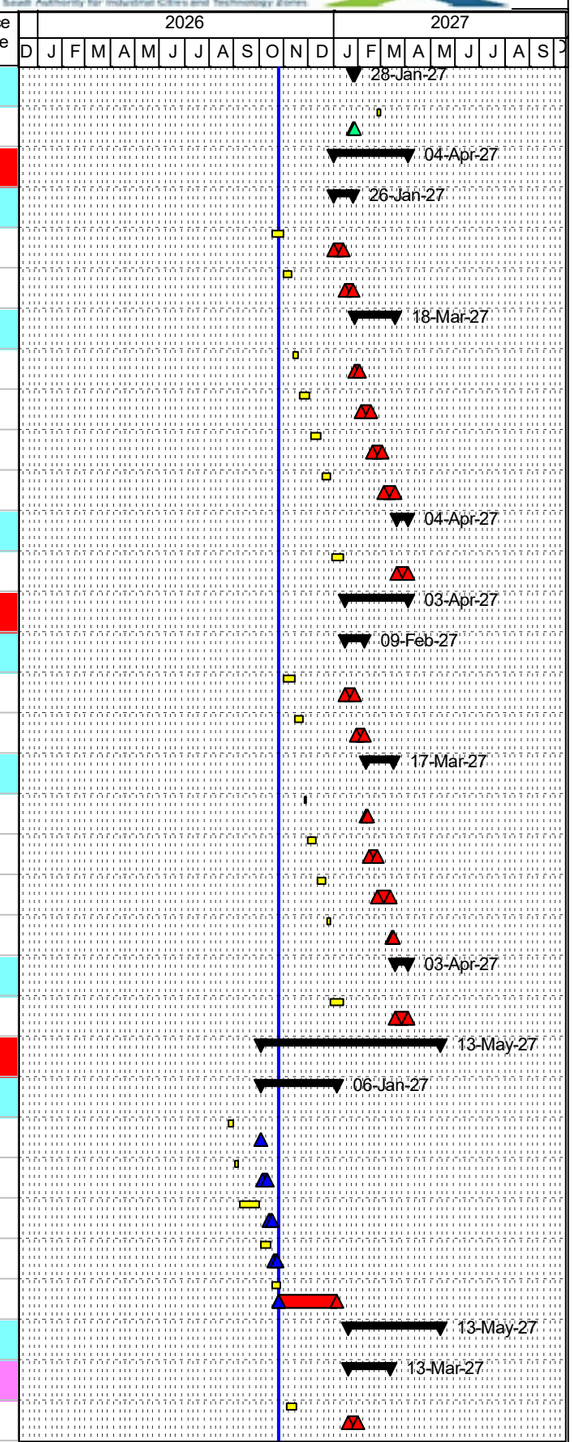

Primary Baseline
Remaining Work
Critical Remaining Work
Actual Work
Baseline Milestone
Milestone
Summary

Date	Revision	Checked	Approved
26-Oct-26	Third Industrial City		


Activity ID	Activity Name	Original Duration	Start	Finish	Budgeted Total Cost	Planned Value Cost	Earned Value Cost	Actual Total Cost	Schedule % Complete	Performance % Complete
CO-UB-CR-160	Thermal & Moisture Protection Work for Control Room	56	01-Feb-27	08-Feb-27	21,971	0	0	0	0%	0%
CO-UB-CR-200	Install For Curtian Wall and Windows and Doors	56	09-Feb-27	16-Feb-27	91,926	0	0	0	0%	0%
CO-UB-CR-240	External Finshing Work (Walls and Floor)	64	17-Feb-27	25-Feb-27	127,277	0	0	0	0%	0%
CO-UB-CR-250	Internal Finshing Work (Walls,Floor and Ceiling)	80	27-Feb-27	13-Mar-27	21,751	0	0	0	0%	0%
Mechanical Work		576	01-Feb-27	28-Apr-27	1,331,986	0	0	0	0%	0%
HVAC System		576	01-Feb-27	28-Apr-27	137,139	0	0	0	0%	0%
CO-UB-CR-170	Install of Refrigerant Piping (fabricated metal ducts with flanges complete with supports,	168	01-Feb-27	24-Feb-27	68,570	0	0	0	0%	0%
CO-UB-CR-260	Install of Mini split actual and Ducted split	160	14-Mar-27	05-Apr-27	30,178	0	0	0	0%	0%
CO-UB-CR-310	Install of Air Grills 150mm x150mm and Air Diffuser 600mm x 600mm	160	06-Apr-27	28-Apr-27	38,392	0	0	0	0%	0%
Fire Fitting System		136	25-Feb-27	20-Mar-27	434,599	0	0	0	0%	0%
CO-UB-CR-180	Installation & Testing of 2 hours Fire rated system for closing the openings between	80	25-Feb-27	08-Mar-27	405,466	0	0	0	0%	0%
CO-UB-CR-270	Install Fire Extinguishers	48	14-Mar-27	20-Mar-27	29,133	0	0	0	0%	0%
Plumbing System		96	14-Mar-27	27-Mar-27	760,248	0	0	0	0%	0%
CO-UB-CR-370	Install of Sanitary Wares Including Relevant Pipes and Fittings	96	14-Mar-27	27-Mar-27	760,248	0	0	0	0%	0%
Electrical Work		376	14-Mar-27	06-May-27	965,706	0	0	0	0%	0%
LV Power		344	14-Mar-27	02-May-27	874,883	0	0	0	0%	0%
CO-UB-CR-190	Install of Distribution board For Control Room	80	14-Mar-27	24-Mar-27	87,096	0	0	0	0%	0%
CO-UB-CR-220	Install of Earting Cable for Control Room	112	25-Mar-27	10-Apr-27	190,403	0	0	0	0%	0%
CO-UB-CR-280	Install of Socket outlet and LED Lighting	152	11-Apr-27	02-May-27	597,384	0	0	0	0%	0%
Fire Detection And Alarm System		280	28-Mar-27	06-May-27	90,824	0	0	0	0%	0%
CO-UB-CR-210	Install of 2C x 1.5 Sqm FR Rated Armored - Cable For Loop Wiring	32	28-Mar-27	31-Mar-27	35,785	0	0	0	0%	0%
CO-UB-CR-230	Install of Transmission Communication cable - Fiber Optics 12Core	32	01-Apr-27	05-Apr-27	17,975	0	0	0	0%	0%
CO-UB-CR-290	Install of power supply system for fire alarm control panel	32	06-Apr-27	10-Apr-27	11,246	0	0	0	0%	0%
CO-UB-CR-300	Install of Fire Alarm Control panel	48	11-Apr-27	17-Apr-27	16,024	0	0	0	0%	0%
CO-UB-CR-320	Installation of the addressable manual call point with operation safety glass breaking	24	18-Apr-27	20-Apr-27	243	0	0	0	0%	0%
CO-UB-CR-330	Install of the photoelectric heat & smoke detector	40	21-Apr-27	26-Apr-27	4,229	0	0	0	0%	0%
CO-UB-CR-340	Install of Sounder With Beacon	40	27-Apr-27	02-May-27	1,190	0	0	0	0%	0%
CO-UB-CR-350	Install of Addressable Control module	32	03-May-27	06-May-27	4,131	0	0	0	0%	0%
Furnitures work		48	08-May-27	13-May-27	443,507	0	0	0	0%	0%
CO-UB-CR-360	Office Chairs,Tables and Stand	48	08-May-27	13-May-27	443,507	0	0	0	0%	0%
Softscape and Planting Works		280	01-May-27	15-Jun-27	3,915,193	0	0	0	0%	0%
CO-LS-PL-160	Planting Works: Planting including plants, forming planting beds, suitable soil, supports,	120	01-May-27	23-May-27	2,361,373	0	0	0	0%	0%
CO-LS-SF-170	Site Furnishings (Seating Bench,Stone Boulders and Gravel)	160	24-May-27	15-Jun-27	1,553,820	0	0	0	0%	0%
Storm Drainage Ponds		488	01-Oct-26 A	05-May-27	8,820,044	0	3,969,020	3,969,053	0%	45%

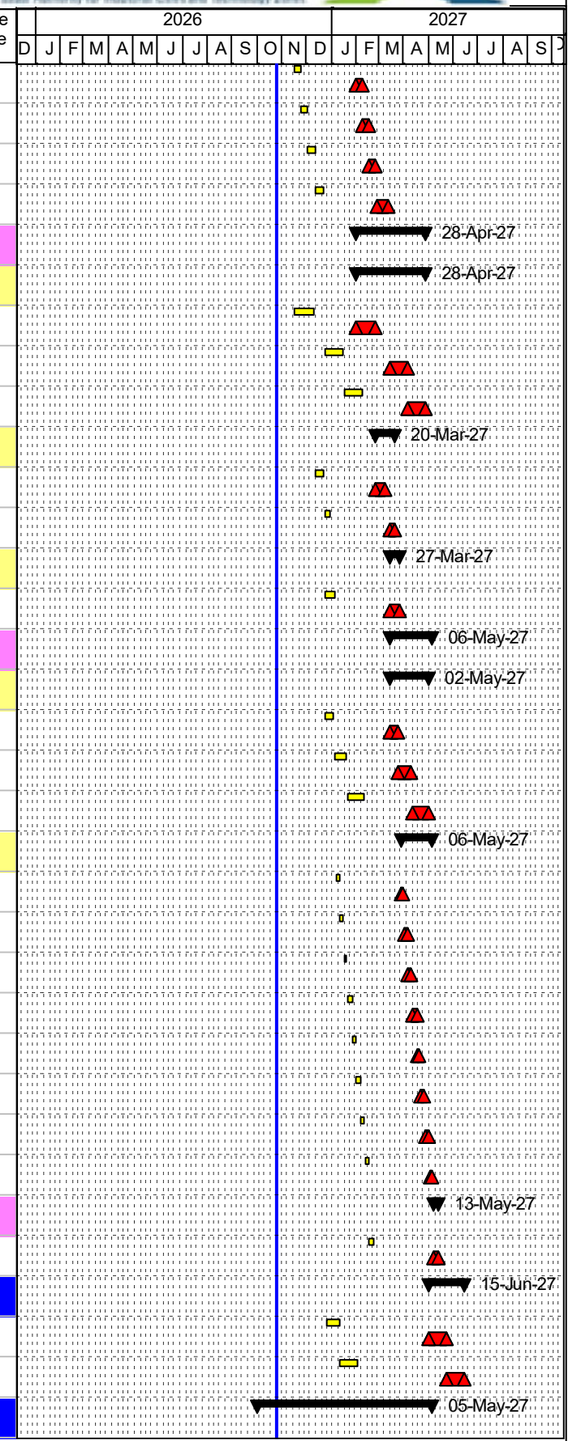

Primary Baseline
Remaining Work
Critical Remaining Work
Actual Work
Baseline Milestone
Milestone
Summary

Date	Revision	Checked	Approved
26-Oct-26	Third Industrial City		

Activity ID	Activity Name	Original Duration	Start	Finish	Budgeted Total Cost	Planned Value Cost	Earned Value Cost	Actual Total Cost	Schedule % Complete	Performance % Complete
CO-SD-PO-100-P1	Excavation & Filling Works - PART 1 for Storm Drainage Ponds	56	01-Oct-26 A	17-Mar-27	4,093,463	0	3,684,116	3,684,116	0%	90%
CO-SD-PO-100-P2	Excavation & Filling Works - PART 2 for Storm Drainage Ponds	136	28-Mar-27	15-Apr-27	4,093,463	0	0	0	0%	0%
CO-SD-PO-110-P1	Finished Grouted Riprap - PART 1 for Storm Drainage Ponds	64	01-Mar-27 A	27-Mar-27	316,560	0	284,904	284,937	0%	90%
CO-SD-PO-110-P2	Finished Grouted Riprap - PART 2 for Storm Drainage Ponds	136	17-Apr-27	05-May-27	316,560	0	0	0	0%	0%
Boundary Fence and Gaurd Room		1536	01-Aug-26 A	13-Jun-27	14,872,951	1,960,769	4,618,279	4,281,518	13.18%	31.05%
Gaurd Room Work		352	18-Apr-27	13-Jun-27	1,497,270	0	0	0	0%	0%
Civil Work		120	18-Apr-27	04-May-27	67,559	0	0	0	0%	0%
A1000	Excavation Work For Guard Room Foundation	40	18-Apr-27	22-Apr-27	2,684	0	0	0	0%	0%
A1010	Pouring for Plain Concrete for Guard Room	8	24-Apr-27	24-Apr-27	2,684	0	0	0	0%	0%
A1020	Pouring R.C Footing for Guard Room	24	25-Apr-27	27-Apr-27	10,083	0	0	0	0%	0%
A1030	Pouring R.C Columns for Guard Room	24	28-Apr-27	01-May-27	3,675	0	0	0	0%	0%
A1040	Pouring Beams and Slab for Guard Room	24	02-May-27	04-May-27	48,433	0	0	0	0%	0%
Finishing Work		232	05-May-27	13-Jun-27	1,429,712	0	0	0	0%	0%
Architectural work		216	05-May-27	10-Jun-27	915,197	0	0	0	0%	0%
A1050	Brick Works for Architectural Works for Guard Rooms	48	05-May-27	11-May-27	21,591	0	0	0	0%	0%
A1060	Thermal & Moisture Protection Work for Architectural Works for Guard Rooms	40	12-May-27	23-May-27	12,891	0	0	0	0%	0%
A1070	Installation of Windows and Doors for Architectural Works for Guard Rooms	40	06-Jun-27	10-Jun-27	49,349	0	0	0	0%	0%
A1080	External Finshing Work (Walls and Floor) for Architectural Works for Guard Rooms	16	30-May-27	31-May-27	109,603	0	0	0	0%	0%
A1090	Internal Finshing Work (Walls,Floor and Ceiling) for Architectural Works for Guard	48	30-May-27	05-Jun-27	721,763	0	0	0	0%	0%
Mechanical Work		64	24-May-27	01-Jun-27	157,994	0	0	0	0%	0%
Drainage System		64	24-May-27	01-Jun-27	44,607	0	0	0	0%	0%
A1110	Installation of Sewage Piping System complete with joints, angles, reducer etc. for	32	24-May-27	27-May-27	33,221	0	0	0	0%	0%
A1120	Installation of all Sanitary Ware for Drainage System for Guard Rooms	32	29-May-27	01-Jun-27	11,386	0	0	0	0%	0%
Water Supply System		64	24-May-27	01-Jun-27	51,133	0	0	0	0%	0%
A1140	Installation of Water Piping System complete with joints, angles, reducer etc. for Water	24	24-May-27	26-May-27	13,381	0	0	0	0%	0%
A1180	Installation oF Water Supply Wares (Water Heater, Faucets, Etc..) for Water Supply	16	27-May-27	29-May-27	12,899	0	0	0	0%	0%
A1240	Installation of water tanks for Water Supply System for Guard Rooms	8	01-Jun-27	01-Jun-27	24,852	0	0	0	0%	0%
HVAC System		24	24-May-27	26-May-27	11,367	0	0	0	0%	0%
A1190	Installation of AC Units for HVAC System for Guard Rooms	8	26-May-27	26-May-27	4,142	0	0	0	0%	0%
A1200	Installation of AC Piping for HVAC System for Guard Rooms	16	24-May-27	25-May-27	7,225	0	0	0	0%	0%
Fire Fighting System		24	24-May-27	26-May-27	50,888	0	0	0	0%	0%
A1220	Installation & Testing of 2 hours Fire Fighting system for Fire Fighting System for Guard	16	24-May-27	25-May-27	29,586	0	0	0	0%	0%
A1230	Installation of Fire Extinguishers for Fire Fighting System for Guard Rooms	8	26-May-27	26-May-27	21,302	0	0	0	0%	0%
Electrical Work		88	24-May-27	05-Jun-27	335,219	0	0	0	0%	0%

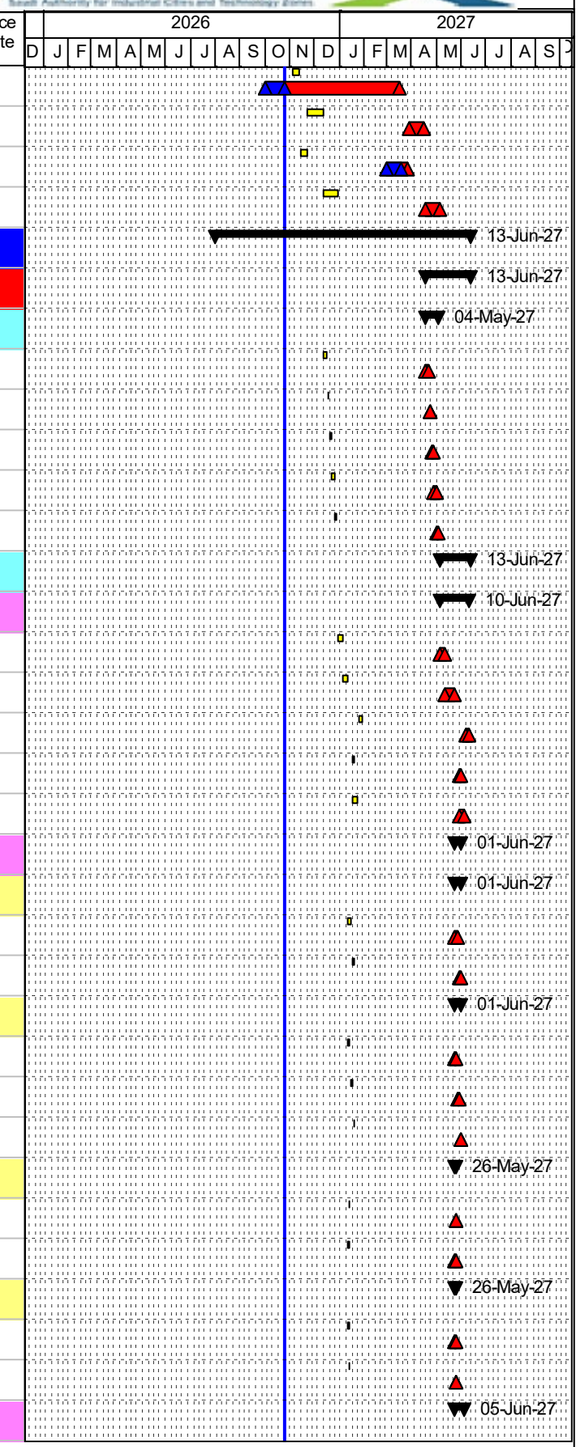


Primary Baseline | Actual Work | Summary
Remaining Work | Baseline Milestone
Critical Remaining Work | Milestone

Date	Revision	Checked	Approved
26-Oct-26	Third Industrial City		

Development of the Technology City in Dharan Project
BL-Update 26-10-2026
WPR UPS LEVEL 5

Activity ID	Activity Name	Original Duration	Start	Finish	Budgeted Total Cost	Planned Value Cost	Earned Value Cost	Actual Total Cost	Schedule % Complete	Performance % Complete
LV Power		72	24-May-27	02-Jun-27	107,021	0	0	0	0%	0%
A1250	Installation of Conduits and Cables for LV System for Gaurd Rooms	40	24-May-27	29-May-27	58,313	0	0	0	0%	0%
A1260	Install of Eletrical Finishes (DBs, Sockets and Lightings) and Termination for LV System for	32	30-May-27	02-Jun-27	48,708	0	0	0	0%	0%
Fire Detection And Alarm System		88	24-May-27	05-Jun-27	228,198	0	0	0	0%	0%
A1340	Installation of Conduits and Cables for Fire Alarm System for Gaurd Rooms	40	24-May-27	29-May-27	135,702	0	0	0	0%	0%
A1350	Installation of Fire Alarm Devices (AMCP, SD,HD, Sounder and Panels) for Fire Alarm	48	30-May-27	05-Jun-27	92,496	0	0	0	0%	0%
Furniture work		16	12-Jun-27	13-Jun-27	21,302	0	0	0	0%	0%
A1100	Office Chairs,Tables and Stand	16	12-Jun-27	13-Jun-27	21,302	0	0	0	0%	0%
Boundary Fence		1464	01-Aug-26 A	02-Jun-27	13,375,680	1,960,769	4,618,279	4,281,518	14.66%	34.53%
Boundary Fence - South		1152	01-Aug-26 A	12-Apr-27	3,343,920	1,006,654	548,551	973,654	30.1%	16.4%
Civil Work		536	01-Aug-26 A	09-Jan-27	1,036,327	1,006,654	492,560	917,633	97.14%	47.53%
CO-SU-FE-N-CI-100	Excavation Work For Boundary Fence South	128	01-Aug-26 A	03-Aug-26 A	66,380	66,380	66,380	66,380	100%	100%
CO-SU-FE-N-CI-110	Pouring for Plain Concrete For Boundary Fence South	112	08-Aug-26 A	13-Aug-26 A	66,380	66,380	66,380	66,380	100%	100%
CO-SU-FE-N-CI-120	Pouring R.C Footing For Boundary Fence South	96	15-Aug-26 A	22-Aug-26 A	312,570	312,570	312,570	312,570	100%	100%
CO-SU-FE-N-CI-130	Pouring R.C Columns For Boundary Fence South	128	26-Sep-26 A	27-Dec-26	472,304	472,304	47,230	472,304	100%	10%
CO-SU-FE-N-CI-140	Pouring Beams For Boundary Fence South	96	27-Dec-26	09-Jan-27	118,694	89,020	0	0	75%	0%
Finishing Work		712	13-Oct-26 A	12-Apr-27	2,307,593	0	55,991	56,021	0%	2.43%
Architictural work		544	13-Oct-26 A	18-Mar-27	1,666,313	0	55,991	56,021	0%	3.36%
CO-SU-FE-N-AR-100	Install Brick Work For Boundary Fence South	152	13-Oct-26 A	31-Jan-27	279,956	0	55,991	56,021	0%	20%
CO-SU-FE-N-AR-110	Insulation For Boundary Fence South	120	16-Feb-27	04-Mar-27	109,999	0	0	0	0%	0%
CO-SU-FE-N-AR-120	Install all the Relevant Cladding and Finishes For Boundary Fence South	72	06-Mar-27	18-Mar-27	1,276,358	0	0	0	0%	0%
Electrical Work		464	01-Feb-27	12-Apr-27	641,279	0	0	0	0%	0%
CO-SU-FE-N-EL-240	Installation of Conduits and Cables for Electricial Works For Boundary Fence South	104	01-Feb-27	15-Feb-27	154,292	0	0	0	0%	0%
CO-SU-FE-N-EL-250	Install, fixings, testing of all electrical finishes and lightings for Electricial Works For	168	20-Mar-27	12-Apr-27	486,987	0	0	0	0%	0%
Boundary Fence - West		1096	01-Aug-26 A	22-Apr-27	3,343,920	622,443	1,601,557	1,360,449	18.61%	47.89%
Civil Work		408	01-Aug-26 A	18-Oct-26 A	1,036,327	622,443	1,036,327	1,036,327	60.06%	100%
CO-SU-FE-N-CI-150	Excavation Work For Boundary Fence West	128	01-Aug-26 A	04-Aug-26 A	66,380	66,380	66,380	66,380	100%	100%
CO-SU-FE-N-CI-160	Pouring for Plain Concrete For Boundary Fence West	104	05-Aug-26 A	10-Aug-26 A	66,380	66,380	66,380	66,380	100%	100%
CO-SU-FE-N-CI-170	Pouring R.C Footing For Boundary Fence West	128	11-Aug-26 A	19-Aug-26 A	312,570	312,570	312,570	312,570	100%	100%
CO-SU-FE-N-CI-180	Pouring R.C Columns For Boundary Fence West	128	26-Sep-26 A	12-Oct-26 A	472,304	177,114	472,304	472,304	37.5%	100%
CO-SU-FE-N-CI-190	Pouring Beams For Boundary Fence West	96	12-Oct-26 A	18-Oct-26 A	118,694	0	118,694	118,694	0%	100%
Finishing Work		680	01-Oct-26 A	22-Apr-27	2,307,593	0	565,230	324,122	0%	24.49%
Architictural work		560	01-Oct-26 A	05-Apr-27	1,666,313	0	565,230	324,122	0%	33.92%
CO-SU-FE-N-AR-130	Install Brick Work For Boundary Fence West	128	01-Oct-26 A	11-Feb-27	279,956	0	265,958	265,919	0%	95%

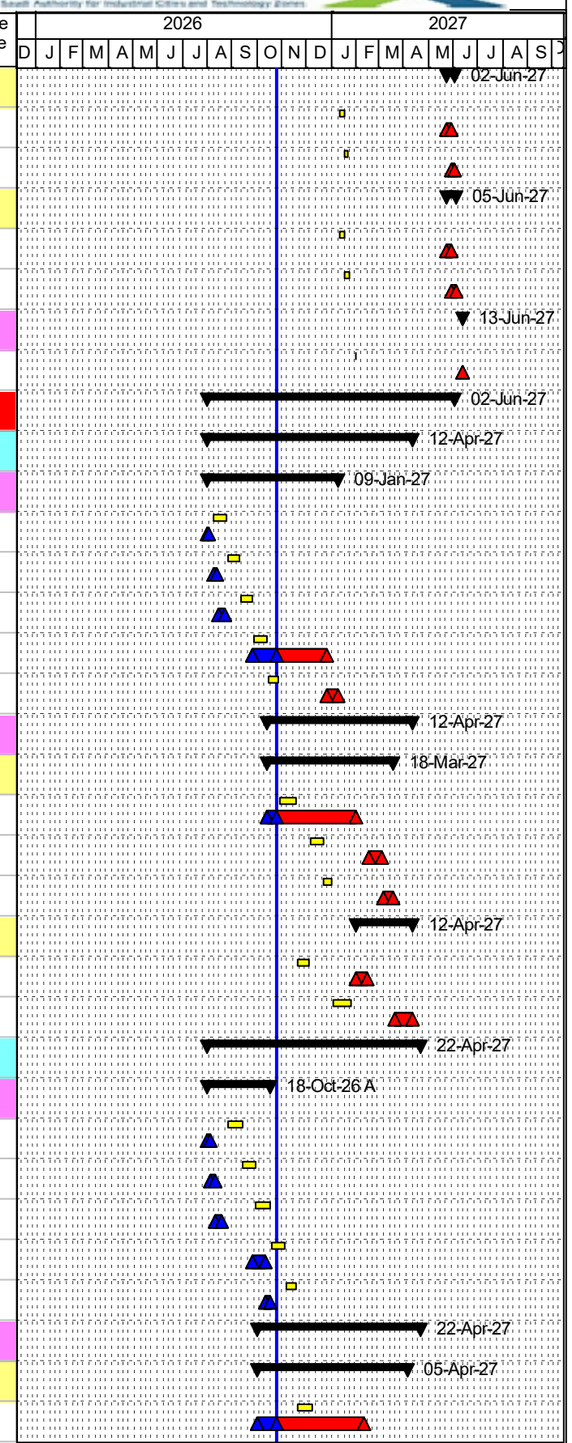


Primary Baseline
Remaining Work
Critical Remaining Work
Actual Work
Baseline Milestone
Milestone
Summary

Date	Revision	Checked	Approved
26-Oct-26	Third Industrial City		

Development of the Technology City in Dharan Project
BL-Update 26-10-2026
WPR UPS LEVEL 5


Activity ID	Activity Name	Original Duration	Start	Finish	Budgeted Total Cost	Planned Value Cost	Earned Value Cost	Actual Total Cost	Schedule % Complete	Performance % Complete
CO-SU-FE-N-AR-140	Insulation For Boundary Fence West	96	13-Oct-26 A	22-Mar-27	109,999	0	44,000	58,203	0%	40%
CO-SU-FE-N-AR-150	Install all the Relevant Cladding and Finishes For Boundary Fence West	96	23-Mar-27	05-Apr-27	1,276,358	0	255,272	0	0%	20%
Electrical Work		432	16-Feb-27	22-Apr-27	641,279	0	0	0	0%	0%
CO-SU-FE-N-EL-260	Installation of Conduits and Cables for Electricial Works For Boundary Fence West	64	16-Feb-27	24-Feb-27	154,292	0	0	0	0%	0%
CO-SU-FE-N-EL-270	Install, fixings, testing of all electrical finishes and lightings for Electricial Works For	72	13-Apr-27	22-Apr-27	486,987	0	0	0	0%	0%
Boundary Fence - North		944	01-Aug-26 A	19-Apr-27	3,343,921	249,973	1,493,863	1,280,139	7.48%	44.67%
Civil Work		376	01-Aug-26 A	23-Jan-27	1,036,327	249,973	917,633	917,633	24.12%	88.55%
CO-SU-FE-N-CI-200	Excavation Work For Boundary Fence North	128	01-Aug-26 A	04-Aug-26 A	66,380	66,380	66,380	66,380	100%	100%
CO-SU-FE-N-CI-210	Pouring for Plain Concrete For Boundary Fence North	104	05-Aug-26 A	11-Aug-26 A	66,380	66,380	66,380	66,380	100%	100%
CO-SU-FE-N-CI-220	Pouring R.C Footing For Boundary Fence North	128	11-Aug-26 A	02-Sep-26 A	312,570	117,214	312,570	312,570	37.5%	100%
CO-SU-FE-N-CI-230	Pouring R.C Columns For Boundary Fence North	128	26-Sep-26 A	12-Oct-26 A	472,304	0	472,304	472,304	0%	100%
CO-SU-FE-N-CI-240	Pouring Beams For Boundary Fence North	96	10-Jan-27	23-Jan-27	118,694	0	0	0	0%	0%
Finishing Work		528	01-Oct-26 A	19-Apr-27	2,307,594	0	576,229	362,505	0%	24.97%
Architictural work		424	01-Oct-26 A	12-Apr-27	1,666,315	0	576,229	362,505	0%	34.58%
CO-SU-FE-N-AR-160	Install Brick Work For Boundary Fence North	112	01-Oct-26 A	20-Feb-27	279,956	0	265,958	139,978	0%	95%
CO-SU-FE-N-AR-170	Insulation For Boundary Fence North	88	23-Mar-27	04-Apr-27	110,000	0	54,999	0	0%	50%
CO-SU-FE-N-AR-180	Install all the Relevant Cladding and Finishes For Boundary Fence North	48	11-Oct-26 A	12-Apr-27	1,276,358	0	255,272	222,527	0%	20%
Electrical Work		344	25-Feb-27	19-Apr-27	641,279	0	0	0	0%	0%
CO-SU-FE-N-EL-280	Installation of Conduits and Cables for Electricial Works For Boundary Fence North	56	25-Feb-27	04-Mar-27	154,292	0	0	0	0%	0%
CO-SU-FE-N-EL-290	Install, fixings, testing of all electrical finishes and lightings for Electricial Works For	48	13-Apr-27	19-Apr-27	486,987	0	0	0	0%	0%
Boundary Fence - East		1080	06-Sep-26 A	02-Jun-27	3,343,920	81,698	974,308	667,275	2.44%	29.14%
Civil Work		360	06-Sep-26 A	03-Feb-27	1,036,327	81,698	752,327	445,330	7.88%	72.6%
CO-SU-FE-N-CI-250	Excavation Work For Boundary Fence East	128	19-Dec-26 A	19-Dec-26 A	66,380	66,380	66,380	66,380	100%	100%
CO-SU-FE-N-CI-260	Pouring for Plain Concrete For Boundary Fence East	104	06-Sep-26 A	20-Sep-26 A	66,380	15,318	66,380	66,380	23.08%	100%
CO-SU-FE-N-CI-270	Pouring R.C Footing For Boundary Fence East	128	21-Sep-26 A	12-Oct-26 A	312,570	0	312,570	312,570	0%	100%
CO-SU-FE-N-CI-280	Pouring R.C Columns For Boundary Fence East	128	26-Sep-26 A	16-Jan-27	472,304	0	306,997	0	0%	65%
CO-SU-FE-N-CI-290	Pouring Beams For Boundary Fence East	80	24-Jan-27	03-Feb-27	118,694	0	0	0	0%	0%
Finishing Work		424	01-Oct-26 A	02-Jun-27	2,307,593	0	221,981	221,946	0%	9.62%
Architictural work		384	01-Oct-26 A	27-May-27	1,666,313	0	221,981	221,946	0%	13.32%
CO-SU-FE-N-AR-190	Install Brick Work For Boundary Fence East	88	08-Oct-26 A	29-Apr-27	279,956	0	111,983	111,947	0%	40%
CO-SU-FE-N-AR-200	Insulation For Boundary Fence East	64	01-Oct-26 A	12-Oct-26 A	109,999	0	109,999	109,999	0%	100%
CO-SU-FE-N-AR-210	Install all the Relevant Cladding and Finishes For Boundary Fence East	72	12-May-27	27-May-27	1,276,358	0	0	0	0%	0%
Electrical Work		192	01-May-27	02-Jun-27	641,279	0	0	0	0%	0%
CO-SU-FE-N-EL-300	Installation of Conduits and Cables for Electricial Works For Boundary Fence East	80	01-May-27	11-May-27	154,292	0	0	0	0%	0%

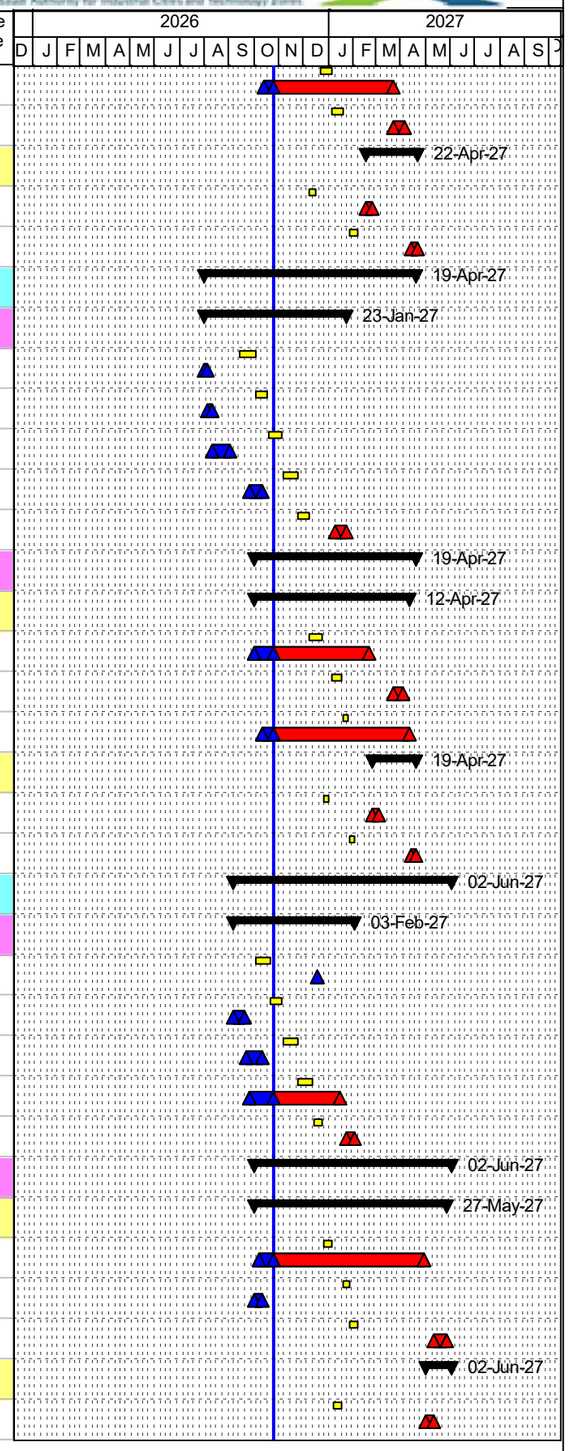

Primary Baseline | Actual Work | Summary
Remaining Work | Baseline Milestone
Critical Remaining Work | Milestone

Date	Revision	Checked	Approved
26-Oct-26	Third Industrial City		

Activity ID	Activity Name	Original Duration	Start	Finish	Budgeted Total Cost	Planned Value Cost	Earned Value Cost	Actual Total Cost	Schedule % Complete	Performance % Complete
CO-SU-FE-N-EL-310	Install, fixings, testing of all electrical finishes and lightings for Electricial Works For	40	29-May-27	02-Jun-27	486,987	0	0	0	0%	0%
Testing and Comissioning		200	14-Jun-27	12-Jul-27	0	0	0	0	0%	0%
Infrastructure Networks		136	19-Jun-27	07-Jul-27	0	0	0	0	0%	0%
Low Voltage Network		96	24-Jun-27	07-Jul-27	0	0	0	0	0%	0%
TC-LV-100	Testing and Commissioning of Low Voltage Network	96	24-Jun-27	07-Jul-27	0	0	0	0	0%	0%
Irrigation Network		96	24-Jun-27	07-Jul-27	0	0	0	0	0%	0%
T/C-IR	Testing and Commissioning of Irrigation Network	96	24-Jun-27	07-Jul-27	0	0	0	0	0%	0%
TSE Network		96	24-Jun-27	07-Jul-27	0	0	0	0	0%	0%
T/C-TSE-10	Testing and Commissioning of TSE Network	96	24-Jun-27	07-Jul-27	0	0	0	0	0%	0%
Potable Water Network		96	24-Jun-27	07-Jul-27	0	0	0	0	0%	0%
T/C-PW	Testing and Commissioning of Potable Water Network	96	24-Jun-27	07-Jul-27	0	0	0	0	0%	0%
Sewage Network		96	24-Jun-27	07-Jul-27	0	0	0	0	0%	0%
T/C-SW	Testing and Commissioning of Sewage Network	96	24-Jun-27	07-Jul-27	0	0	0	0	0%	0%
Storm Drainage Network		96	24-Jun-27	07-Jul-27	0	0	0	0	0%	0%
T/C-DPO	Testing and Commissioning of Storm Drainage Ponds	96	24-Jun-27	07-Jul-27	0	0	0	0	0%	0%
T/C-SD	Testing and Commissioning of Storm Drainage Ponds and Storm Drainage Network	96	24-Jun-27	07-Jul-27	0	0	0	0	0%	0%
Street Lighting Network		96	19-Jun-27	01-Jul-27	0	0	0	0	0%	0%
T/C-SL	Testing and Commissioning of Street Lighting Network	96	19-Jun-27	01-Jul-27	0	0	0	0	0%	0%
Telecom and Light Current Network		96	19-Jun-27	01-Jul-27	0	0	0	0	0%	0%
T/C-TE	Testing and Commissioning of Telecom and Light Current Networks	96	19-Jun-27	01-Jul-27	0	0	0	0	0%	0%
Medium Voltage Network		96	19-Jun-27	01-Jul-27	0	0	0	0	0%	0%
T/C-MV	Testing and Commissioning of Medium Voltage Network	96	19-Jun-27	01-Jul-27	0	0	0	0	0%	0%
Road Works		96	19-Jun-27	01-Jul-27	0	0	0	0	0%	0%
T/C-RD	Testing and Commissioning of Road Works	96	19-Jun-27	01-Jul-27	0	0	0	0	0%	0%
Utility Buildings		200	14-Jun-27	12-Jul-27	0	0	0	0	0%	0%
T/C-CTV	Testing and Commissioning of Guard Room and Boundary Fence	128	14-Jun-27	01-Jul-27	0	0	0	0	0%	0%
T/C-CTV10	Testing and Commissioning of Utility Buildings	128	24-Jun-27	12-Jul-27	0	0	0	0	0%	0%
T/C-CTV20	Testing and Commissioning of Softscape And Planting	128	16-Jun-27	04-Jul-27	0	0	0	0	0%	0%
Handing over and close out		192	19-Jun-27	15-Jul-27	0	0	0	0	0%	0%
As-Built		192	19-Jun-27	15-Jul-27	0	0	0	0	0%	0%
HO-100	Submission As-Built Drawing For Sewage Network	80	24-Jun-27	05-Jul-27	0	0	0	0	0%	0%
HO-130	Submission As-Built Drawing For Pond	80	24-Jun-27	05-Jul-27	0	0	0	0	0%	0%
HO-140	Submission As-Built Drawing For Roads Network	80	19-Jun-27	29-Jun-27	0	0	0	0	0%	0%
HO-150	Submission As-Built Drawing For Street Lighting Network	80	19-Jun-27	29-Jun-27	0	0	0	0	0%	0%

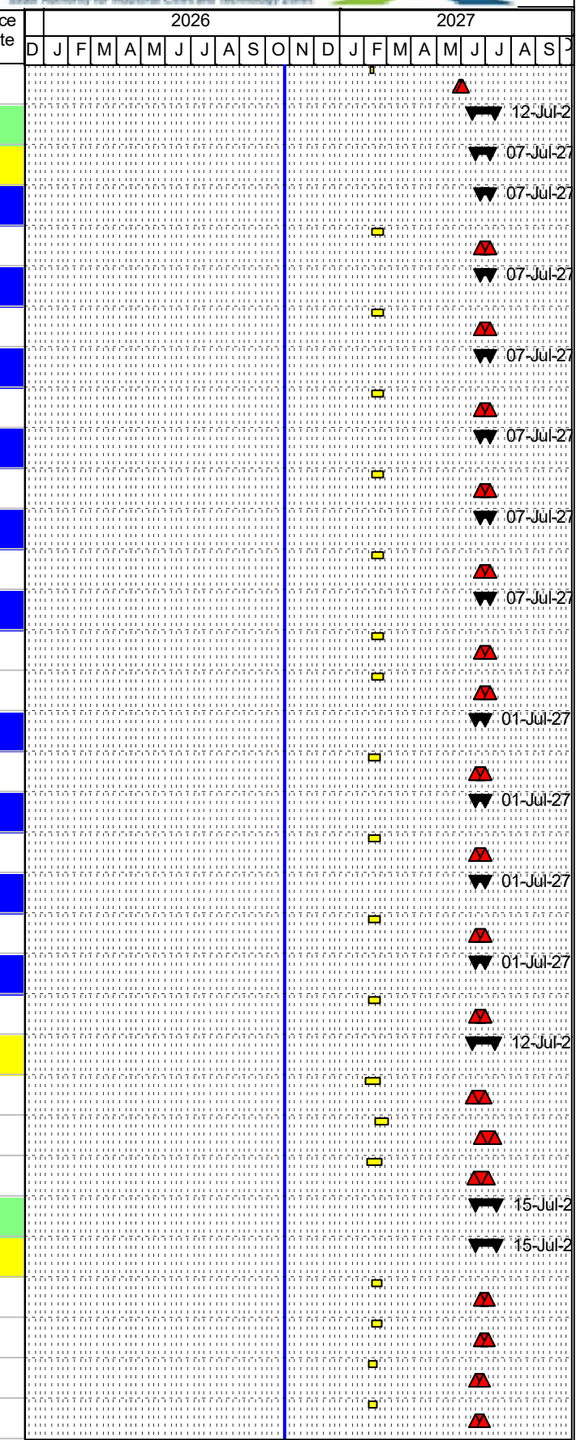


Primary Baseline
Remaining Work
Critical Remaining Work
Actual Work
Baseline Milestone
Milestone
Summary

Date	Revision	Checked	Approved
26-Oct-26	Third Industrial City		

Development of the Technology City in Dharan Project
BL-Update 26-10-2026
WPR UPS LEVEL 5

Activity ID	Activity Name	Original Duration	Start	Finish	Budgeted Total Cost	Planned Value Cost	Earned Value Cost	Actual Total Cost	Schedule % Complete	Performance % Complete
HO-160	Submission As-Built Drawing For Telecom and Light Current Networks	80	19-Jun-27	29-Jun-27	0	0	0	0	0%	0%
HO-170	Submission As-Built Drawing For Medium Voltage Network	56	08-Jul-27	15-Jul-27	0	0	0	0	0%	0%
HO-180	Submission As-Built Drawing For Irrigation Network	80	24-Jun-27	05-Jul-27	0	0	0	0	0%	0%
HO-190	As-Built Drawing For Potable Water Network	56	08-Jul-27	15-Jul-27	0	0	0	0	0%	0%
HO-200	Submission As-Built Drawing For Storm Network	80	24-Jun-27	05-Jul-27	0	0	0	0	0%	0%
HO-210	Submission As-Built Drawing For Utility Buildings	64	04-Jul-27	12-Jul-27	0	0	0	0	0%	0%
De-Mobilization Works		144	21-Jun-27	11-Jul-27	0	0	0	0	0%	0%
HO-120	Remove material stock & Storage area	64	03-Jul-27	11-Jul-27	0	0	0	0	0%	0%
HO-220	Removing Portable Caravan	56	24-Jun-27	01-Jul-27	0	0	0	0	0%	0%
HO-230	Remove Temporary Car Shades	80	21-Jun-27	01-Jul-27	0	0	0	0	0%	0%
Handing Over		160	23-Jun-27	15-Jul-27	0	0	0	0	0%	0%
HO-110	Final Testing Work	56	08-Jul-27	15-Jul-27	0	0	0	0	0%	0%
HO-240	Final Walkthrough and Inspection	64	23-Jun-27	01-Jul-27	0	0	0	0	0%	0%
HO-250	Review B.O.Q Qty. to ensure compliance with the actual status	64	23-Jun-27	01-Jul-27	0	0	0	0	0%	0%
HO-260	Review FIR Approval to ensure compliance with the actual status	64	23-Jun-27	01-Jul-27	0	0	0	0	0%	0%
HO-270	Review the sample drawing to ensure compliance with the actual status	64	23-Jun-27	01-Jul-27	0	0	0	0	0%	0%
HO-280	Punch List Completion	64	03-Jul-27	11-Jul-27	0	0	0	0	0%	0%

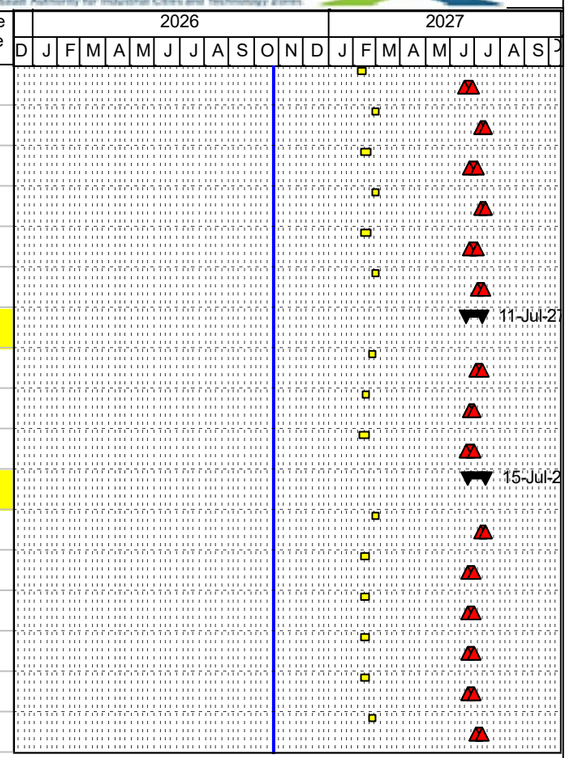

Primary Baseline
Remaining Work
Critical Remaining Work
Actual Work
Baseline Milestone
Milestone
Summary

Date	Revision	Checked	Approved
26-Oct-26	Third Industrial City		
