
egis ENJAZCO

MKH2-02-003 - Completion of Infrastructure Works at the Second Industrial City in Makkah UP 31
WBS L5

MODON مدن


Activity ID	Activity Name	Original Duration	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Schedule % Complete	Performance % Complete	Variance - BL Project Finish Date
MKH2-02-003 - Completion of Infrastructure W		489	15-Feb-26	14-Aug-27	15-Feb-26 A	26-Sep-27	28,097,288.28	39,183,289.00	52,025,516.00	54.01%	75.32%	-36
KEY MILESTONES		489	15-Feb-26	14-Aug-27	15-Feb-26 A	26-Sep-27	0.00	0.00	0.00	0%	0%	-36
GENERAL MILESTONES		489	15-Feb-26	14-Aug-27	15-Feb-26 A	26-Sep-27	0.00	0.00	0.00	0%	0%	-36
MKH2-02-003-MS-1080	Project Commencement Date	0	15-Feb-26		15-Feb-26 A		0.00	0.00	0.00	100%	100%	0
MKH2-02-003-MS-1090	Project Kick Off Meeting/NTP	0	15-Feb-26		15-Feb-26 A		0.00	0.00	0.00	100%	100%	0
MKH2-02-003-MS-1100	Project Completion	0		14-Aug-27		26-Sep-27	0.00	0.00	0.00	0%	0%	-36
CONTRACTUAL MILESTONE		477	14-Mar-26	14-Aug-27	01-Mar-26 A	26-Sep-27	0.00	0.00	0.00	0%	0%	-36
MKH2-02-003-MS-1000	Completion of Mobilization	0		14-Mar-26		06-Jun-26 A	0.00	0.00	0.00	100%	100%	-66
MKH2-02-003-MS-1010	Baseline Programme Approval	0		14-Mar-26		01-Mar-26 A	0.00	0.00	0.00	100%	100%	12
MKH2-02-003-MS-1020	Prequalification & Material Approval	0		14-Apr-26		06-Jun-26 A	0.00	0.00	0.00	100%	100%	-42
MKH2-02-003-MS-1030	Completion of Long lead Materials I	0		16-Aug-26		29-Aug-26 A	0.00	0.00	0.00	100%	100%	-11
MKH2-02-003-MS-1040	Completion of Road Works	0		14-Dec-26		07-Feb-27	0.00	0.00	0.00	0%	0%	-47
MKH2-02-003-MS-1050	Completion of Open Drain Channel	0		14-Jun-27		26-Jul-27	0.00	0.00	0.00	0%	0%	-36
MKH2-02-003-MS-1060	Completion of All Works	0		14-Aug-27		26-Sep-27	0.00	0.00	0.00	0%	0%	-36
MKH2-02-003-MS-1070	Final Handover	0		14-Aug-27		26-Sep-27	0.00	0.00	0.00	0%	0%	-36
MOBILIZATION		99	15-Feb-26	14-Mar-26	15-Feb-26 A	06-Jun-26 A	0.00	0.00	0.00	0%	0%	-66
TOPOGRAPHIC SURVEY		7	15-Feb-26	23-Feb-26	15-Feb-26 A	23-Feb-26 A	0.00	0.00	0.00	0%	0%	0
MKH2-02-003-MB-1380	Site Survey Works	7	15-Feb-26	23-Feb-26	15-Feb-26 A	23-Feb-26 A	0.00	0.00	0.00	100%	100%	0
SITE FACILITIES & OFFICES		23	15-Feb-26	14-Mar-26	15-Feb-26 A	28-Feb-26 A	0.00	0.00	0.00	0%	0%	12
MKH2-02-003-MB-1000	Site Layout Plan	4	15-Feb-26	18-Feb-26	15-Feb-26 A	18-Feb-26 A	0.00	0.00	0.00	100%	100%	0
MKH2-02-003-MB-1010	Clear & Grub for Offices & Access R	3	19-Feb-26	23-Feb-26	15-Feb-26 A	19-Feb-26 A	0.00	0.00	0.00	100%	100%	2
MKH2-02-003-MB-1020	Construct Site Access Roads	4	19-Feb-26	24-Feb-26	19-Feb-26 A	24-Feb-26 A	0.00	0.00	0.00	100%	100%	0
MKH2-02-003-MB-1030	Construct Temporary Fence	7	24-Feb-26	03-Mar-26	15-Feb-26 A	19-Feb-26 A	0.00	0.00	0.00	100%	100%	9
MKH2-02-003-MB-1040	Construct Site Offices & Storage	14	25-Feb-26	12-Mar-26	15-Feb-26 A	22-Feb-26 A	0.00	0.00	0.00	100%	100%	16
MKH2-02-003-MB-1050	Install Project Signs	8	25-Feb-26	05-Mar-26	25-Feb-26 A	28-Feb-26 A	0.00	0.00	0.00	100%	100%	5
MKH2-02-003-MB-1060	Install Site Facilities	4	04-Mar-26	08-Mar-26	15-Feb-26 A	19-Feb-26 A	0.00	0.00	0.00	100%	100%	13
MKH2-02-003-MB-1070	Electrical Works & Connections	6	04-Mar-26	10-Mar-26	15-Feb-26 A	19-Feb-26 A	0.00	0.00	0.00	100%	100%	15
MKH2-02-003-MB-1080	Construct Parking Sheds	6	04-Mar-26	10-Mar-26	15-Feb-26 A	21-Feb-26 A	0.00	0.00	0.00	100%	100%	14
MKH2-02-003-MB-1090	Manpower Mobalization	5	09-Mar-26	14-Mar-26	15-Feb-26 A	21-Feb-26 A	0.00	0.00	0.00	100%	100%	17
MKH2-02-003-MB-1100	Equipment Mobalization	7	07-Mar-26	14-Mar-26	15-Feb-26 A	22-Feb-26 A	0.00	0.00	0.00	100%	100%	17
PRELIMINARY SUBMITTALS		99	19-Feb-26	14-Mar-26	15-Feb-26 A	06-Jun-26 A	0.00	0.00	0.00	0%	0%	-66
PREPARATIONS & SUBMITTAL BY CONTRACTORS		88	19-Feb-26	01-Mar-26	15-Feb-26 A	04-Jun-26 A	0.00	0.00	0.00	0%	0%	-76
MKH2-02-003-MB-1120	Advance Payemnt Application	8	19-Feb-26	01-Mar-26	15-Feb-26 A	16-Feb-26 A	0.00	0.00	0.00	100%	100%	10
MKH2-02-003-MB-1130	Performance bond as per the Cond	8	19-Feb-26	01-Mar-26	15-Feb-26 A	19-Feb-26 A	0.00	0.00	0.00	100%	100%	7
MKH2-02-003-MB-1140	Insurances as per the Conditions of	8	19-Feb-26	01-Mar-26	18-Feb-26 A	21-Feb-26 A	0.00	0.00	0.00	100%	100%	6
MKH2-02-003-MB-1150	Contractor's Plant and Equipment Ir	8	19-Feb-26	01-Mar-26	18-Feb-26 A	21-Feb-26 A	0.00	0.00	0.00	100%	100%	6
MKH2-02-003-MB-1160	Third Party liability Insurance includi	8	19-Feb-26	01-Mar-26	18-Feb-26 A	21-Feb-26 A	0.00	0.00	0.00	100%	100%	6
MKH2-02-003-MB-1170	Workmen's Compensation Employe	8	19-Feb-26	01-Mar-26	18-Feb-26 A	21-Feb-26 A	0.00	0.00	0.00	100%	100%	6
MKH2-02-003-MB-1180	Advance Payment Bond as per the	8	19-Feb-26	01-Mar-26	18-Feb-26 A	21-Feb-26 A	0.00	0.00	0.00	100%	100%	6
MKH2-02-003-MB-1190	Preparation and Submittal of Detail	8	19-Feb-26	01-Mar-26	17-Feb-26 A	28-Feb-26 A	0.00	0.00	0.00	100%	100%	1
MKH2-02-003-MB-1200	Preparation and Submittal of Projec	8	19-Feb-26	01-Mar-26	17-Feb-26 A	18-Feb-26 A	0.00	0.00	0.00	100%	100%	8
MKH2-02-003-MB-1210	Submission of Contractor Project Q	8	19-Feb-26	01-Mar-26	23-Feb-26 A	25-Feb-26 A	0.00	0.00	0.00	100%	100%	3
MKH2-02-003-MB-1220	Submission of Construction Safety	8	19-Feb-26	01-Mar-26	19-Feb-26 A	23-Feb-26 A	0.00	0.00	0.00	100%	100%	5
MKH2-02-003-MB-1230	Preparation and Submittal of Organ	8	19-Feb-26	01-Mar-26	05-Mar-26 A	05-Mar-26 A	0.00	0.00	0.00	100%	100%	-4
MKH2-02-003-MB-1240	Preparation and Submittal of Comm	8	19-Feb-26	01-Mar-26	03-Jun-26 A	04-Jun-26 A	0.00	0.00	0.00	100%	100%	-76
APPROVALS BY EMPLOYERS		99	02-Mar-26	14-Mar-26	17-Feb-26 A	06-Jun-26 A	0.00	0.00	0.00	0%	0%	-66
MKH2-02-003-MB-1250	Approval of Payemnt Application	11	02-Mar-26	14-Mar-26	17-Feb-26 A	18-Feb-26 A	0.00	0.00	0.00	100%	100%	19
MKH2-02-003-MB-1260	Approval of Performance bond as p	11	02-Mar-26	14-Mar-26	19-Feb-26 A	21-Feb-26 A	0.00	0.00	0.00	100%	100%	17
MKH2-02-003-MB-1270	Approval of Insurances as per the C	11	02-Mar-26	14-Mar-26	22-Feb-26 A	26-Feb-26 A	0.00	0.00	0.00	100%	100%	13
MKH2-02-003-MB-1280	Approval of Contractor's Plant and E	11	02-Mar-26	14-Mar-26	22-Feb-26 A	26-Feb-26 A	0.00	0.00	0.00	100%	100%	13
MKH2-02-003-MB-1290	Approval of Third Party liability Insur	11	02-Mar-26	14-Mar-26	18-Feb-26 A	26-Feb-26 A	0.00	0.00	0.00	100%	100%	13
MKH2-02-003-MB-1300	Approval of Workmen's Compensat	11	02-Mar-26	14-Mar-26	22-Feb-26 A	26-Feb-26 A	0.00	0.00	0.00	100%	100%	13

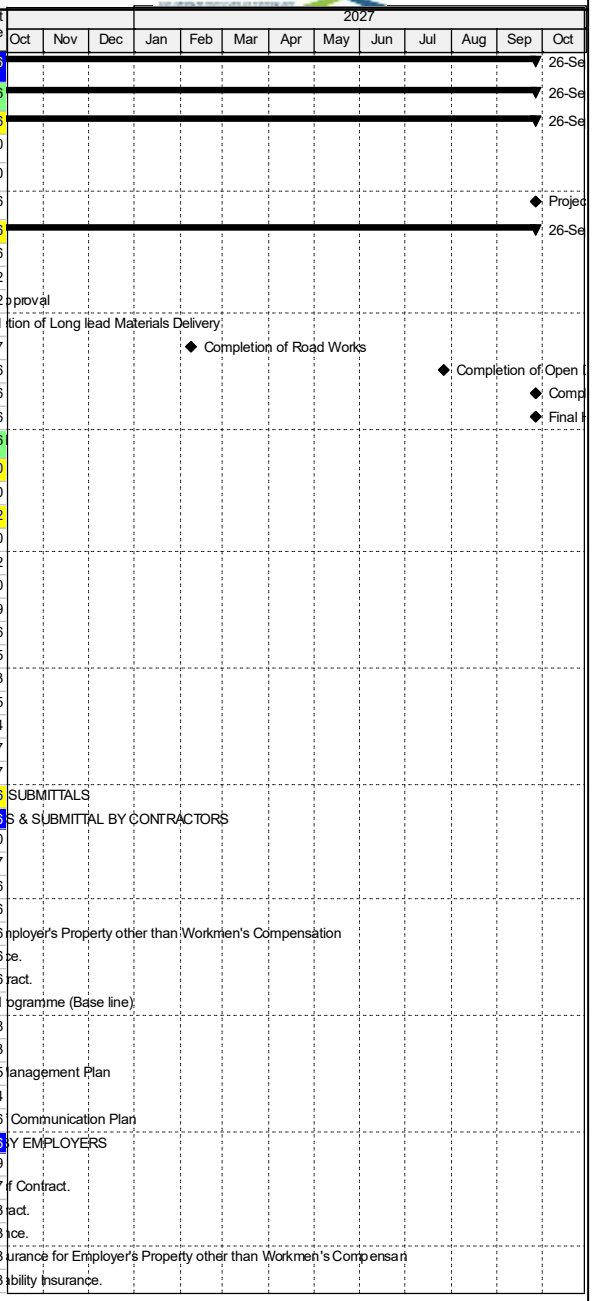

Actual Work | Critical Remaining Work | Remaining Work | Milestone

Date	Revision	Checked	Approved


Activity ID	Activity Name	Original Duration	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Schedule % Complete	Performance % Complete	Variance - BL Project Finish Date
MKH2-02-003-MB-1310	Approval of Advance Payment Bon	11	02-Mar-26	14-Mar-26	22-Feb-26 A	26-Feb-26 A	0.00	0.00	0.00	100%	100%	13
MKH2-02-003-MB-1320	Approval of Detailed Work Order Pr	11	02-Mar-26	14-Mar-26	28-Feb-26 A	01-Mar-26 A	0.00	0.00	0.00	100%	100%	11
MKH2-02-003-MB-1330	Approval of Project Execution Plan	11	02-Mar-26	14-Mar-26	18-Feb-26 A	19-Feb-26 A	0.00	0.00	0.00	100%	100%	18
MKH2-02-003-MB-1340	Approval of Contractor Project Qual	11	02-Mar-26	14-Mar-26	16-Mar-26 A	29-Mar-26 A	0.00	0.00	0.00	100%	100%	-10
MKH2-02-003-MB-1350	Approval of Construction Safety & E	11	02-Mar-26	14-Mar-26	24-Feb-26 A	09-Mar-26 A	0.00	0.00	0.00	100%	100%	4
MKH2-02-003-MB-1360	Approval of Organization Chart	11	02-Mar-26	14-Mar-26	05-Mar-26 A	05-Mar-26 A	0.00	0.00	0.00	100%	100%	7
MKH2-02-003-MB-1370	Approval of Communication Plan	11	02-Mar-26	14-Mar-26	04-Jun-26 A	06-Jun-26 A	0.00	0.00	0.00	100%	100%	-66
ENGINEERING		133	19-Feb-26	14-Apr-26	17-Feb-26 A	22-Jul-26 A	1,560,765.48	1,560,765.48	1,560,765.48	100%	100%	-82
SHOP DRAWINGS		100	24-Feb-26	14-Apr-26	18-Feb-26 A	07-Jun-26 A	0.00	0.00	0.00	0%	0%	-43
SHOP DRAWINGS SUBMISSION		93	24-Feb-26	05-Apr-26	18-Feb-26 A	04-Jun-26 A	0.00	0.00	0.00	0%	0%	-49
SHOP DRAWING SUBMITTALS FOR ROAD WORKS		85	24-Feb-26	14-Mar-26	18-Feb-26 A	04-Jun-26 A	0.00	0.00	0.00	0%	0%	-65
MKH2-02-003-EN-1090	Shop DWG Submittal for Topograph	8	24-Feb-26	04-Mar-26	24-Feb-26 A	28-Feb-26 A	0.00	0.00	0.00	100%	100%	4
MKH2-02-003-EN-1100	Shop DWG Submittal for Road Lay	8	05-Mar-26	14-Mar-26	25-Feb-26 A	28-Feb-26 A	0.00	0.00	0.00	100%	100%	12
MKH2-02-003-EN-1110	Shop DWG Submittal for Typical Cr	8	05-Mar-26	14-Mar-26	26-Feb-26 A	28-Feb-26 A	0.00	0.00	0.00	100%	100%	12
MKH2-02-003-EN-1120	Shop DWG Submittal for Road Sett	8	05-Mar-26	14-Mar-26	25-Feb-26 A	28-Feb-26 A	0.00	0.00	0.00	100%	100%	12
MKH2-02-003-EN-1130	Shop DWG Submittal for Road Prof	8	05-Mar-26	14-Mar-26	25-Feb-26 A	28-Feb-26 A	0.00	0.00	0.00	100%	100%	12
MKH2-02-003-EN-1140	Shop DWG Submittal for Grading L	8	05-Mar-26	14-Mar-26	26-Feb-26 A	28-Feb-26 A	0.00	0.00	0.00	100%	100%	12
MKH2-02-003-EN-1150	Shop DWG Submittal for Curb Setti	8	05-Mar-26	14-Mar-26	03-Jun-26 A	04-Jun-26 A	0.00	0.00	0.00	100%	100%	-65
MKH2-02-003-EN-1160	Shop DWG Submittal for Signing &	8	05-Mar-26	14-Mar-26	18-Feb-26 A	19-Feb-26 A	0.00	0.00	0.00	100%	100%	18
MKH2-02-003-EN-1170	Shop DWG Submittal for Standards	8	05-Mar-26	14-Mar-26	18-Feb-26 A	19-Feb-26 A	0.00	0.00	0.00	100%	100%	18
SHOP DRAWINGS SUBMITTALS FOR ELECTRICAL NETWORK		8	15-Mar-26	26-Mar-26	03-Jun-26 A	04-Jun-26 A	0.00	0.00	0.00	0%	0%	-57
MKH2-02-003-EN-1180	Shop DWG Submittal for Low Volta	8	15-Mar-26	26-Mar-26	03-Jun-26 A	04-Jun-26 A	0.00	0.00	0.00	100%	100%	-57
MKH2-02-003-EN-1190	Shop DWG Submittal for Street Ligl	8	15-Mar-26	26-Mar-26	03-Jun-26 A	04-Jun-26 A	0.00	0.00	0.00	100%	100%	-57
SHOP DRAWINGS SUBMITTALS FOR EARTHING SYSTEM		8	28-Mar-26	05-Apr-26	03-Jun-26 A	04-Jun-26 A	0.00	0.00	0.00	0%	0%	-49
MKH2-02-003-EN-1200	Shop DWG Submittal for Earthing S	8	28-Mar-26	05-Apr-26	03-Jun-26 A	04-Jun-26 A	0.00	0.00	0.00	100%	100%	-49
SHOP DRAWINGS SUBMITTALS FOR ROAD LIGHTING SYSTEM		8	28-Mar-26	05-Apr-26	16-Mar-26 A	18-Mar-26 A	0.00	0.00	0.00	0%	0%	12
MKH2-02-003-EN-1210	Shop DWG Submittal for Street Ligl	8	28-Mar-26	05-Apr-26	16-Mar-26 A	18-Mar-26 A	0.00	0.00	0.00	100%	100%	12
MKH2-02-003-EN-1220	Shop DWG Submittal for Street Ligl	8	28-Mar-26	05-Apr-26	16-Mar-26 A	18-Mar-26 A	0.00	0.00	0.00	100%	100%	12
MKH2-02-003-EN-1230	Shop DWG Submittal for Street Ligl	8	28-Mar-26	05-Apr-26	16-Mar-26 A	18-Mar-26 A	0.00	0.00	0.00	100%	100%	12
MKH2-02-003-EN-1240	Shop DWG Submittal for Street Ligl	8	28-Mar-26	05-Apr-26	16-Mar-26 A	18-Mar-26 A	0.00	0.00	0.00	100%	100%	12
SHOP DRAWINGS SUBMITTALS FOR OPENCHANNEL		69	15-Mar-26	26-Mar-26	28-Feb-26 A	04-Jun-26 A	0.00	0.00	0.00	0%	0%	-57
MKH2-02-003-EN-1250	Shop DWG Submittal for Open Cha	8	15-Mar-26	26-Mar-26	28-Feb-26 A	02-Mar-26 A	0.00	0.00	0.00	100%	100%	18
MKH2-02-003-EN-1260	Shop DWG Submittal for Typical Cr	8	15-Mar-26	26-Mar-26	28-Feb-26 A	02-Mar-26 A	0.00	0.00	0.00	100%	100%	18
MKH2-02-003-EN-1270	Shop DWG Submittal for Open Cha	8	15-Mar-26	26-Mar-26	28-Feb-26 A	02-Mar-26 A	0.00	0.00	0.00	100%	100%	18
MKH2-02-003-EN-1280	Shop DWG Submittal for Grading L	8	15-Mar-26	26-Mar-26	03-Jun-26 A	04-Jun-26 A	0.00	0.00	0.00	100%	100%	-57
MKH2-02-003-EN-1290	Shop DWG Submittal for Standards	8	15-Mar-26	26-Mar-26	03-Jun-26 A	04-Jun-26 A	0.00	0.00	0.00	100%	100%	-57
SHOP DRAWINGS APPROVALS		97	05-Mar-26	14-Apr-26	18-Feb-26 A	07-Jun-26 A	0.00	0.00	0.00	0%	0%	-43
SHOP DRAWING APPROVALS FOR ROAD WORKS		89	05-Mar-26	25-Mar-26	18-Feb-26 A	07-Jun-26 A	0.00	0.00	0.00	0%	0%	-60
MKH2-02-003-EN-1300	Shop DWG Approval for Topograph	7	05-Mar-26	12-Mar-26	22-Apr-26 A	23-Apr-26 A	0.00	0.00	0.00	100%	100%	-33
MKH2-02-003-EN-1310	Shop DWG Approval for Road Layo	7	15-Mar-26	25-Mar-26	01-Mar-26 A	08-Mar-26 A	0.00	0.00	0.00	100%	100%	12
MKH2-02-003-EN-1320	Shop DWG Approval for Typical Cro	7	15-Mar-26	25-Mar-26	06-Jun-26 A	07-Jun-26 A	0.00	0.00	0.00	100%	100%	-60
MKH2-02-003-EN-1330	Shop DWG Approval for Road Setti	7	15-Mar-26	25-Mar-26	06-Jun-26 A	07-Jun-26 A	0.00	0.00	0.00	100%	100%	-60
MKH2-02-003-EN-1340	Shop DWG Approval for Road Profi	7	15-Mar-26	25-Mar-26	01-Mar-26 A	08-Mar-26 A	0.00	0.00	0.00	100%	100%	12
MKH2-02-003-EN-1350	Shop DWG Approval for Grading La	7	15-Mar-26	25-Mar-26	06-Jun-26 A	07-Jun-26 A	0.00	0.00	0.00	100%	100%	-60
MKH2-02-003-EN-1360	Shop DWG Approval for Curb Settir	7	15-Mar-26	25-Mar-26	06-Jun-26 A	07-Jun-26 A	0.00	0.00	0.00	100%	100%	-60
MKH2-02-003-EN-1370	Shop DWG Approval for Signing & I	7	15-Mar-26	25-Mar-26	18-Feb-26 A	19-Feb-26 A	0.00	0.00	0.00	100%	100%	25
MKH2-02-003-EN-1380	Shop DWG Approval for Standards	7	15-Mar-26	25-Mar-26	19-Feb-26 A	19-Feb-26 A	0.00	0.00	0.00	100%	100%	25
SHOP DRAWINGS APPROVALS FOR ELECTRICAL NETWORK		7	28-Mar-26	04-Apr-26	04-Jun-26 A	06-Jun-26 A	0.00	0.00	0.00	0%	0%	-51
MKH2-02-003-EN-1390	Shop DWG Approval for Low Voltag	7	28-Mar-26	04-Apr-26	04-Jun-26 A	06-Jun-26 A	0.00	0.00	0.00	100%	100%	-51
MKH2-02-003-EN-1400	Shop DWG Approval for Street Ligh	7	28-Mar-26	04-Apr-26	04-Jun-26 A	06-Jun-26 A	0.00	0.00	0.00	100%	100%	-51
SHOP DRAWINGS APPROVALS FOR EARTHING SYSTEM		7	06-Apr-26	13-Apr-26	04-Jun-26 A	06-Jun-26 A	0.00	0.00	0.00	0%	0%	-43
MKH2-02-003-EN-1410	Shop DWG Approval for Earthing S	7	06-Apr-26	13-Apr-26	04-Jun-26 A	06-Jun-26 A	0.00	0.00	0.00	100%	100%	-43
SHOP DRAWINGS APPROVALS FOR ROAD LIGHTING SYSTEM		20	06-Apr-26	14-Apr-26	18-Mar-26 A	09-Apr-26 A	0.00	0.00	0.00	0%	0%	4
MKH2-02-003-EN-1420	Shop DWG Approval for Street Ligh	8	06-Apr-26	14-Apr-26	18-Mar-26 A	30-Mar-26 A	0.00	0.00	0.00	100%	100%	13

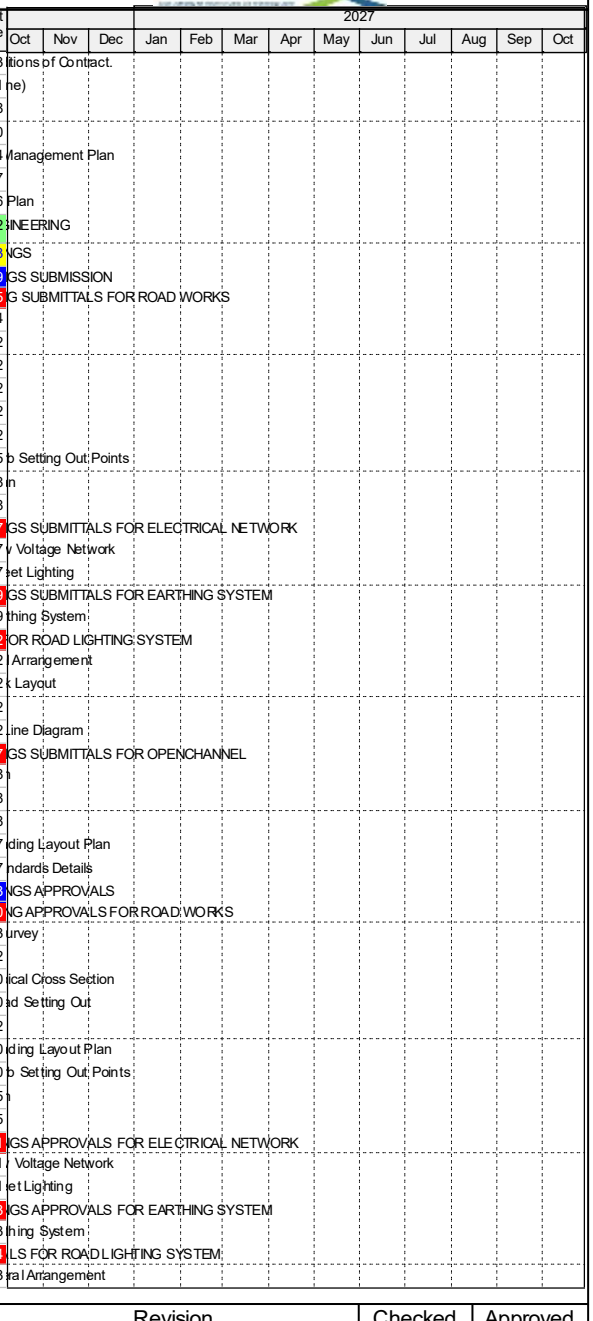

Actual Work
Remaining Work
Critical Remaining Work
Milestone

Date	Revision	Checked	Approved


Activity ID	Activity Name	Original Duration	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Schedule % Complete	Performance % Complete	Variance - BL Project Finish Date
MKH2-02-003-EN-1430	Shop DWG Approval for Street Ligh	8	06-Apr-26	14-Apr-26	08-Apr-26 A	09-Apr-26 A	0.00	0.00	0.00	100%	100%	4
MKH2-02-003-EN-1440	Shop DWG Approval for Street Ligh	8	06-Apr-26	14-Apr-26	18-Mar-26 A	30-Mar-26 A	0.00	0.00	0.00	100%	100%	13
MKH2-02-003-EN-1450	Shop DWG Approval for Street Ligh	8	06-Apr-26	14-Apr-26	18-Mar-26 A	30-Mar-26 A	0.00	0.00	0.00	100%	100%	13
SHOP DRAWINGS APPROVALS FOR OPENCHANNEL		82	28-Mar-26	05-Apr-26	02-Mar-26 A	07-Jun-26 A	0.00	0.00	0.00	0%	0%	-51
MKH2-02-003-EN-1460	Shop DWG Approval for Open Chai	8	28-Mar-26	05-Apr-26	02-Mar-26 A	03-Mar-26 A	0.00	0.00	0.00	100%	100%	25
MKH2-02-003-EN-1470	Shop DWG Approval for Typical Cro	8	28-Mar-26	05-Apr-26	02-Mar-26 A	02-Mar-26 A	0.00	0.00	0.00	100%	100%	26
MKH2-02-003-EN-1480	Shop DWG Approval for Open Chai	8	28-Mar-26	05-Apr-26	02-Mar-26 A	09-Mar-26 A	0.00	0.00	0.00	100%	100%	20
MKH2-02-003-EN-1490	Shop DWG Approval for Grading La	8	28-Mar-26	05-Apr-26	06-Jun-26 A	07-Jun-26 A	0.00	0.00	0.00	100%	100%	-51
MKH2-02-003-EN-1500	Shop DWG Approval for Standards	8	28-Mar-26	05-Apr-26	06-Jun-26 A	07-Jun-26 A	0.00	0.00	0.00	100%	100%	-51
METHOD STATEMENTS		133	19-Feb-26	13-Apr-26	17-Feb-26 A	22-Jul-26 A	0.00	0.00	0.00	0%	0%	-83
METHOD STATEMENT SUBMITTAL		91	19-Feb-26	28-Mar-26	17-Feb-26 A	21-Jul-26 A	0.00	0.00	0.00	0%	0%	-95
Civil Works		91	19-Feb-26	08-Mar-26	17-Feb-26 A	21-Jul-26 A	0.00	0.00	0.00	0%	0%	-109
Road Works		91	19-Feb-26	08-Mar-26	17-Feb-26 A	21-Jul-26 A	0.00	0.00	0.00	0%	0%	-109
MKH2-02-003-EN-1000	Preparation & Submission of Metho	14	19-Feb-26	08-Mar-26	01-Mar-26 A	08-Mar-26 A	0.00	0.00	0.00	100%	100%	0
MKH2-02-003-EN-1010	Preparation & Submission of Metho	14	19-Feb-26	08-Mar-26	17-Feb-26 A	18-Feb-26 A	0.00	0.00	0.00	100%	100%	14
MKH2-02-003-EN-1020	Preparation & Submission of Metho	14	19-Feb-26	08-Mar-26	23-Feb-26 A	25-Feb-26 A	0.00	0.00	0.00	100%	100%	9
MKH2-02-003-EN-1060	Preparation & Submission of Metho	14	19-Feb-26	08-Mar-26	14-May-26 A	21-Jul-26 A	0.00	0.00	0.00	100%	100%	-109
MKH2-02-003-EN-1070	Preparation & Submission of Metho	14	19-Feb-26	08-Mar-26	23-Mar-26 A	26-Mar-26 A	0.00	0.00	0.00	100%	100%	-12
Open Drain Channel		14	19-Feb-26	08-Mar-26	20-Apr-26 A	21-Apr-26 A	0.00	0.00	0.00	0%	0%	-35
MKH2-02-003-EN-2230	Preparation & Submission of Metho	14	19-Feb-26	08-Mar-26	20-Apr-26 A	21-Apr-26 A	0.00	0.00	0.00	100%	100%	-35
Box Culvert		14	19-Feb-26	08-Mar-26	01-Mar-26 A	08-Mar-26 A	0.00	0.00	0.00	0%	0%	0
MKH2-02-003-EN-2330	Preparation & Submission of Metho	14	19-Feb-26	08-Mar-26	01-Mar-26 A	08-Mar-26 A	0.00	0.00	0.00	100%	100%	0
Electrical Works		80	09-Mar-26	28-Mar-26	25-Feb-26 A	04-Jun-26 A	0.00	0.00	0.00	0%	0%	-56
Street Lighting Works		80	09-Mar-26	28-Mar-26	25-Feb-26 A	04-Jun-26 A	0.00	0.00	0.00	0%	0%	-56
MKH2-02-003-EN-5000	Preparation & Submission of Metho	14	09-Mar-26	28-Mar-26	25-Feb-26 A	09-Mar-26 A	0.00	0.00	0.00	100%	100%	13
MKH2-02-003-EN-5010	Preparation & Submission of Metho	14	09-Mar-26	28-Mar-26	06-Apr-26 A	13-Apr-26 A	0.00	0.00	0.00	100%	100%	-14
MKH2-02-003-EN-5020	Preparation & Submission of Metho	14	09-Mar-26	28-Mar-26	03-Jun-26 A	04-Jun-26 A	0.00	0.00	0.00	100%	100%	-56
METHOD STATEMENT APPROVAL		119	09-Mar-26	13-Apr-26	19-Feb-26 A	22-Jul-26 A	0.00	0.00	0.00	0%	0%	-83
Civil Works		119	09-Mar-26	28-Mar-26	19-Feb-26 A	22-Jul-26 A	0.00	0.00	0.00	0%	0%	-97
Road Works		119	09-Mar-26	28-Mar-26	19-Feb-26 A	22-Jul-26 A	0.00	0.00	0.00	0%	0%	-97
MKH2-02-003-EN-5030	Approval of Method Statement for I	14	09-Mar-26	28-Mar-26	25-Mar-26 A	28-Mar-26 A	0.00	0.00	0.00	100%	100%	0
MKH2-02-003-EN-5040	Approval of Method Statement for I	12	09-Mar-26	28-Mar-26	19-Feb-26 A	23-Feb-26 A	0.00	0.00	0.00	100%	100%	23
MKH2-02-003-EN-5050	Approval of Method Statement for I	14	09-Mar-26	28-Mar-26	25-Mar-26 A	28-Mar-26 A	0.00	0.00	0.00	100%	100%	0
MKH2-02-003-EN-5060	Approval of Method Statement for T	14	09-Mar-26	28-Mar-26	21-Jul-26 A	22-Jul-26 A	0.00	0.00	0.00	100%	100%	-97
MKH2-02-003-EN-5070	Approval of Method Statement for I	14	09-Mar-26	28-Mar-26	16-Jun-26 A	16-Jun-26 A	0.00	0.00	0.00	100%	100%	-66
Open Drain Channel		14	09-Mar-26	28-Mar-26	15-Jun-26 A	15-Jun-26 A	0.00	0.00	0.00	0%	0%	-65
MKH2-02-003-EN-5080	Approval of Method Statement for I	14	09-Mar-26	28-Mar-26	15-Jun-26 A	15-Jun-26 A	0.00	0.00	0.00	100%	100%	-65
Box Culvert		14	09-Mar-26	28-Mar-26	11-Mar-26 A	29-Mar-26 A	0.00	0.00	0.00	0%	0%	-1
MKH2-02-003-EN-5090	Approval of Method Statement for I	14	09-Mar-26	28-Mar-26	11-Mar-26 A	29-Mar-26 A	0.00	0.00	0.00	100%	100%	-1
Electrical Works		89	29-Mar-26	13-Apr-26	25-Mar-26 A	15-Jun-26 A	0.00	0.00	0.00	0%	0%	-51
Street Lighting Works		89	29-Mar-26	13-Apr-26	25-Mar-26 A	15-Jun-26 A	0.00	0.00	0.00	0%	0%	-51
MKH2-02-003-EN-5100	Approval of Method Statement for I	14	29-Mar-26	13-Apr-26	25-Mar-26 A	28-Mar-26 A	0.00	0.00	0.00	100%	100%	14
MKH2-02-003-EN-5110	Approval of Method Statement for I	14	29-Mar-26	13-Apr-26	19-May-26 A	15-Jun-26 A	0.00	0.00	0.00	100%	100%	-51
MKH2-02-003-EN-5120	Approval of Method Statement for I	14	29-Mar-26	13-Apr-26	04-Jun-26 A	06-Jun-26 A	0.00	0.00	0.00	100%	100%	-43
PRE-QUALIFICATION & MATERIAL		96	15-Mar-26	14-Apr-26	02-Mar-26 A	06-Jun-26 A	1,560,765.48	1,560,765.48	1,560,765.48	100%	100%	-42
PRE-QUALIFICATION		45	15-Mar-26	30-Mar-26	02-Mar-26 A	29-Mar-26 A	0.00	0.00	0.00	0%	0%	1
ROAD WORKS-CIVIL		29	15-Mar-26	30-Mar-26	03-Mar-26 A	29-Mar-26 A	0.00	0.00	0.00	0%	0%	1
STEEL REINFORCEMENT		11	15-Mar-26	30-Mar-26	03-Mar-26 A	04-Mar-26 A	0.00	0.00	0.00	0%	0%	19
MKH2-02-003-EN-1510	Pre-Qualification Submittal for Steel	5	15-Mar-26	19-Mar-26	03-Mar-26 A	04-Mar-26 A	0.00	0.00	0.00	100%	100%	13
MKH2-02-003-EN-1520	Pre-Qualification Approval for Steel	6	24-Mar-26	30-Mar-26	03-Mar-26 A	04-Mar-26 A	0.00	0.00	0.00	100%	100%	19
READY MIX CONCRETE		11	15-Mar-26	30-Mar-26	29-Mar-26 A	29-Mar-26 A	0.00	0.00	0.00	0%	0%	1
MKH2-02-003-EN-1530	Pre-Qualification Submittal for Read	5	15-Mar-26	19-Mar-26	29-Mar-26 A	29-Mar-26 A	0.00	0.00	0.00	100%	100%	-5
MKH2-02-003-EN-1540	Pre-Qualification Approval for Ready	6	24-Mar-26	30-Mar-26	29-Mar-26 A	29-Mar-26 A	0.00	0.00	0.00	100%	100%	1
WATER PROOFING		11	15-Mar-26	30-Mar-26	10-Mar-26 A	11-Mar-26 A	0.00	0.00	0.00	0%	0%	13
MKH2-02-003-EN-1550	Pre-Qualification Submittal for Wate	5	15-Mar-26	19-Mar-26	10-Mar-26 A	11-Mar-26 A	0.00	0.00	0.00	100%	100%	7

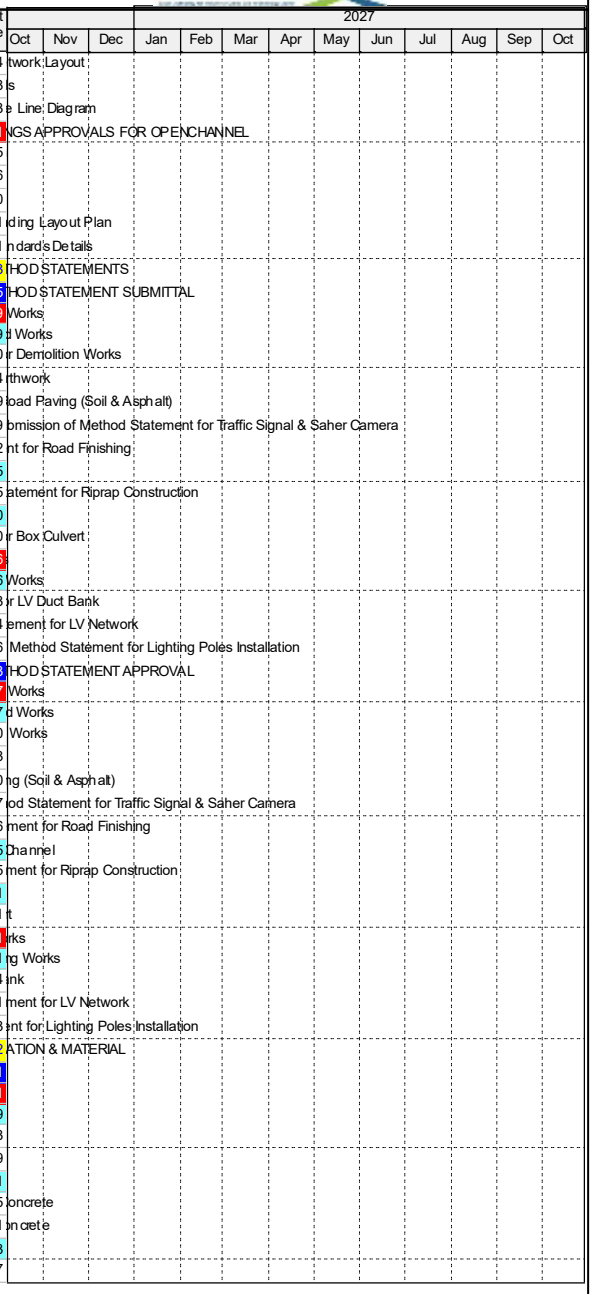

Actual Work
Remaining Work
Critical Remaining Work
Milestone

Date	Revision	Checked	Approved

Activity ID	Activity Name	Original Duration	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Schedule % Complete	Performance % Complete	Variance - BL Project Finish Date
MKH2-02-003-EN-1560	Pre-Qualification Approval for Water	6	24-Mar-26	30-Mar-26	11-Mar-26 A	11-Mar-26 A	0.00	0.00	0.00	100%	100%	13
AGGREGATE BASE COURSE		11	15-Mar-26	30-Mar-26	17-Mar-26 A	18-Mar-26 A	0.00	0.00	0.00	0%	0%	7
MKH2-02-003-EN-1570	Pre-Qualification Submittal for Aggr	5	15-Mar-26	19-Mar-26	17-Mar-26 A	18-Mar-26 A	0.00	0.00	0.00	100%	100%	1
MKH2-02-003-EN-1580	Pre-Qualification Approval for Aggre	6	24-Mar-26	30-Mar-26	18-Mar-26 A	18-Mar-26 A	0.00	0.00	0.00	100%	100%	7
BITU,INOUS BASE & WEARING COURSE		15	15-Mar-26	30-Mar-26	08-Mar-26 A	24-Mar-26 A	0.00	0.00	0.00	0%	0%	5
MKH2-02-003-EN-1590	Pre-Qualification Submittal for Bitun	5	15-Mar-26	19-Mar-26	08-Mar-26 A	09-Mar-26 A	0.00	0.00	0.00	100%	100%	9
MKH2-02-003-EN-1600	Pre-Qualification Approval for Bitum	6	24-Mar-26	30-Mar-26	10-Mar-26 A	24-Mar-26 A	0.00	0.00	0.00	100%	100%	5
PRE-CAST CONCRETE CURBS		11	15-Mar-26	30-Mar-26	10-Mar-26 A	10-Mar-26 A	0.00	0.00	0.00	0%	0%	14
MKH2-02-003-EN-1610	Pre-Qualification Submittal for Preca	5	15-Mar-26	19-Mar-26	10-Mar-26 A	10-Mar-26 A	0.00	0.00	0.00	100%	100%	8
MKH2-02-003-EN-1620	Pre-Qualification Approval for Preca	6	24-Mar-26	30-Mar-26	10-Mar-26 A	10-Mar-26 A	0.00	0.00	0.00	100%	100%	14
INTERLOCKING PAVING BLOCKS		11	15-Mar-26	30-Mar-26	10-Mar-26 A	10-Mar-26 A	0.00	0.00	0.00	0%	0%	14
MKH2-02-003-EN-1630	Pre-Qualification Submittal for Interl	5	15-Mar-26	19-Mar-26	10-Mar-26 A	10-Mar-26 A	0.00	0.00	0.00	100%	100%	8
MKH2-02-003-EN-1640	Pre-Qualification Approval for Interlo	6	24-Mar-26	30-Mar-26	10-Mar-26 A	10-Mar-26 A	0.00	0.00	0.00	100%	100%	14
PAVEMENT MARKING		15	15-Mar-26	30-Mar-26	10-Mar-26 A	12-Mar-26 A	0.00	0.00	0.00	0%	0%	12
MKH2-02-003-EN-1650	Pre-Qualification Submittal for Pave	5	15-Mar-26	19-Mar-26	10-Mar-26 A	11-Mar-26 A	0.00	0.00	0.00	100%	100%	7
MKH2-02-003-EN-1660	Pre-Qualification Approval for Paver	6	24-Mar-26	30-Mar-26	11-Mar-26 A	12-Mar-26 A	0.00	0.00	0.00	100%	100%	12
TRAFFIC SIGNS		11	15-Mar-26	30-Mar-26	11-Mar-26 A	14-Mar-26 A	0.00	0.00	0.00	0%	0%	11
MKH2-02-003-EN-1670	Pre-Qualification Submittal for Traffi	5	15-Mar-26	19-Mar-26	11-Mar-26 A	14-Mar-26 A	0.00	0.00	0.00	100%	100%	5
MKH2-02-003-EN-1680	Pre-Qualification Approval for Traffic	6	24-Mar-26	30-Mar-26	11-Mar-26 A	14-Mar-26 A	0.00	0.00	0.00	100%	100%	11
ELECTRICAL NETWORK		34	15-Mar-26	30-Mar-26	02-Mar-26 A	15-Mar-26 A	0.00	0.00	0.00	0%	0%	10
PIPE FOR DUCT		15	15-Mar-26	30-Mar-26	14-Mar-26 A	15-Mar-26 A	0.00	0.00	0.00	0%	0%	10
MKH2-02-003-EN-1690	Pre-Qualification Submittal for Pipe	5	15-Mar-26	19-Mar-26	14-Mar-26 A	15-Mar-26 A	0.00	0.00	0.00	100%	100%	4
MKH2-02-003-EN-1700	Pre-Qualification Approval for Pipe f	6	24-Mar-26	30-Mar-26	15-Mar-26 A	15-Mar-26 A	0.00	0.00	0.00	100%	100%	10
LOW VOLTAGE CABLES		11	15-Mar-26	30-Mar-26	02-Mar-26 A	07-Mar-26 A	0.00	0.00	0.00	0%	0%	17
MKH2-02-003-EN-1710	Pre-Qualification Submittal for Low	5	15-Mar-26	19-Mar-26	02-Mar-26 A	05-Mar-26 A	0.00	0.00	0.00	100%	100%	12
MKH2-02-003-EN-1720	Pre-Qualification Approval for Low \	6	24-Mar-26	30-Mar-26	05-Mar-26 A	07-Mar-26 A	0.00	0.00	0.00	100%	100%	17
EARTHING SYSTEM		15	15-Mar-26	30-Mar-26	12-Mar-26 A	15-Mar-26 A	0.00	0.00	0.00	0%	0%	10
MKH2-02-003-EN-1730	Pre-Qualification Submittal for Earth	5	15-Mar-26	19-Mar-26	12-Mar-26 A	14-Mar-26 A	0.00	0.00	0.00	100%	100%	5
MKH2-02-003-EN-1740	Pre-Qualification Approval for Earthi	6	24-Mar-26	30-Mar-26	14-Mar-26 A	15-Mar-26 A	0.00	0.00	0.00	100%	100%	10
LOW VOLTAGE DISTRIBUTION PANNEL		11	15-Mar-26	30-Mar-26	09-Mar-26 A	11-Mar-26 A	0.00	0.00	0.00	0%	0%	13
MKH2-02-003-EN-1750	Pre-Qualification Submittal for Distril	5	15-Mar-26	19-Mar-26	09-Mar-26 A	09-Mar-26 A	0.00	0.00	0.00	100%	100%	9
MKH2-02-003-EN-1760	Pre-Qualification Approval for Distrib	6	24-Mar-26	30-Mar-26	09-Mar-26 A	11-Mar-26 A	0.00	0.00	0.00	100%	100%	13
LIGHTING POLES		14	15-Mar-26	30-Mar-26	02-Mar-26 A	08-Mar-26 A	0.00	0.00	0.00	0%	0%	16
MKH2-02-003-EN-1770	Pre-Qualification Submittal for Light	5	15-Mar-26	19-Mar-26	02-Mar-26 A	05-Mar-26 A	0.00	0.00	0.00	100%	100%	12
MKH2-02-003-EN-1780	Pre-Qualification Approval for Lighti	6	24-Mar-26	30-Mar-26	05-Mar-26 A	08-Mar-26 A	0.00	0.00	0.00	100%	100%	16
LIGHTINH PANNELS/FEEDER PILLERS		11	15-Mar-26	30-Mar-26	09-Mar-26 A	11-Mar-26 A	0.00	0.00	0.00	0%	0%	13
MKH2-02-003-EN-1790	Pre-Qualification Submittal for Light	5	15-Mar-26	19-Mar-26	09-Mar-26 A	09-Mar-26 A	0.00	0.00	0.00	100%	100%	9
MKH2-02-003-EN-1800	Pre-Qualification Approval for Lighti	6	24-Mar-26	30-Mar-26	09-Mar-26 A	11-Mar-26 A	0.00	0.00	0.00	100%	100%	13
STREET LIGHTING LUMINAIRE		14	15-Mar-26	30-Mar-26	02-Mar-26 A	08-Mar-26 A	0.00	0.00	0.00	0%	0%	16
MKH2-02-003-EN-1810	Pre-Qualification Submittal for Light	5	15-Mar-26	19-Mar-26	02-Mar-26 A	05-Mar-26 A	0.00	0.00	0.00	100%	100%	12
MKH2-02-003-EN-1820	Pre-Qualification Approval for Lighti	6	24-Mar-26	30-Mar-26	05-Mar-26 A	08-Mar-26 A	0.00	0.00	0.00	100%	100%	16
OPPEN CHANNEL		11	15-Mar-26	30-Mar-26	08-Mar-26 A	11-Mar-26 A	0.00	0.00	0.00	0%	0%	13
RIPRAP MATERIAL		11	15-Mar-26	30-Mar-26	08-Mar-26 A	11-Mar-26 A	0.00	0.00	0.00	0%	0%	13
MKH2-02-003-EN-1830	Pre-Qualification Submittal for RIP-F	5	15-Mar-26	19-Mar-26	08-Mar-26 A	09-Mar-26 A	0.00	0.00	0.00	100%	100%	9
MKH2-02-003-EN-1840	Pre-Qualification Approval for RIP-F	6	24-Mar-26	30-Mar-26	09-Mar-26 A	11-Mar-26 A	0.00	0.00	0.00	100%	100%	13
ACCESSORIES FOR RIPRAP		11	15-Mar-26	30-Mar-26	08-Mar-26 A	11-Mar-26 A	0.00	0.00	0.00	0%	0%	13
MKH2-02-003-EN-1850	Pre-Qualification Submittal for Acce	5	15-Mar-26	19-Mar-26	08-Mar-26 A	09-Mar-26 A	0.00	0.00	0.00	100%	100%	9
MKH2-02-003-EN-1860	Pre-Qualification Approval for Acces	6	24-Mar-26	30-Mar-26	09-Mar-26 A	11-Mar-26 A	0.00	0.00	0.00	100%	100%	13
MATERIAL SUBMITTAL		73	31-Mar-26	14-Apr-26	08-Mar-26 A	06-Jun-26 A	1,560,765.48	1,560,765.48	1,560,765.48	100%	100%	-42
ROAD WORKS-CIVIL		43	31-Mar-26	12-Apr-26	08-Mar-26 A	16-May-26 A	780,382.74	780,382.74	780,382.74	100%	100%	-29
STEEL REINFORCEMENT		15	31-Mar-26	12-Apr-26	09-Mar-26 A	09-Mar-26 A	86,709.19	86,709.19	86,709.19	100%	100%	26
MKH2-02-003-EN-1870	Material Submittal for Steel Reinforc	5	31-Mar-26	05-Apr-26	09-Mar-26 A	09-Mar-26 A	0.00	0.00	0.00	100%	100%	20
MKH2-02-003-EN-1880	Material Approval for Steel Reinforc	6	06-Apr-26	12-Apr-26	09-Mar-26 A	09-Mar-26 A	86,709.19	86,709.19	86,709.19	100%	100%	26
READY MIX CONCRETE		11	31-Mar-26	12-Apr-26	29-Mar-26 A	29-Mar-26 A	86,709.19	86,709.19	86,709.19	100%	100%	12
MKH2-02-003-EN-1890	Material Submittal Submittal for Rea	5	31-Mar-26	05-Apr-26	29-Mar-26 A	29-Mar-26 A	0.00	0.00	0.00	100%	100%	6

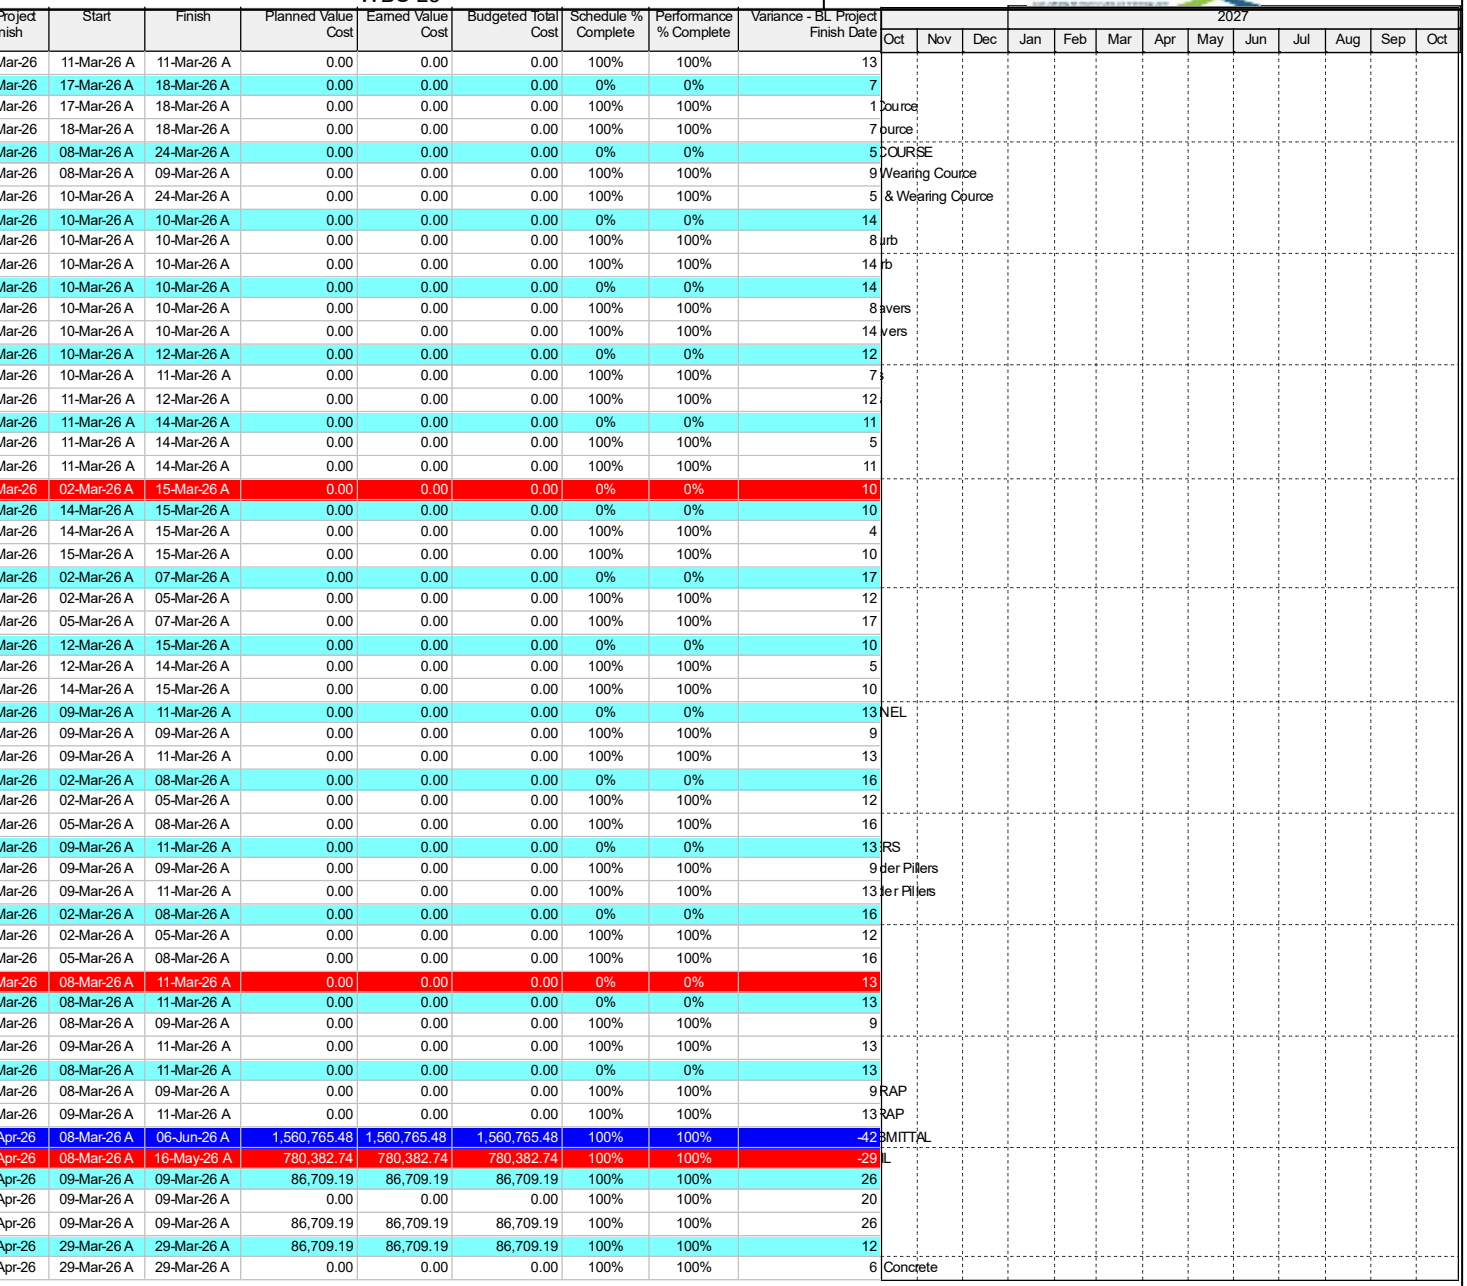

Actual Work
Remaining Work
Critical Remaining Work
Milestone


Date	Revision	Checked	Approved

egis ENJAZCO

MKH2-02-003 - Completion of Infrastructure Works at the Second Industrial City in Makkah UP 31
WBS L5

MODON مدن

Activity ID	Activity Name	Original Duration	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Schedule % Complete	Performance % Complete	Variance - BL Project Finish Date
MKH2-02-003-EN-1900	Material Approval for Ready Mixed	6	06-Apr-26	12-Apr-26	29-Mar-26 A	29-Mar-26 A	86,709.19	86,709.19	86,709.19	100%	100%	12
WATER PROOFING		11	31-Mar-26	12-Apr-26	28-Mar-26 A	28-Mar-26 A	86,709.19	86,709.19	86,709.19	100%	100%	13
MKH2-02-003-EN-1910	Material Submittal for Water Proof i	5	31-Mar-26	05-Apr-26	28-Mar-26 A	28-Mar-26 A	0.00	0.00	0.00	100%	100%	7
MKH2-02-003-EN-1920	Material Approval for Water Proofin	6	06-Apr-26	12-Apr-26	28-Mar-26 A	28-Mar-26 A	86,709.19	86,709.19	86,709.19	100%	100%	13
AGGREGATE BASE COURSE		11	31-Mar-26	12-Apr-26	17-Mar-26 A	24-Mar-26 A	86,709.19	86,709.19	86,709.19	100%	100%	16
MKH2-02-003-EN-1930	Material Submittal for Aggregate Ba	5	31-Mar-26	05-Apr-26	17-Mar-26 A	18-Mar-26 A	0.00	0.00	0.00	100%	100%	12
MKH2-02-003-EN-1940	Material Approval for Aggregate Ba	6	06-Apr-26	12-Apr-26	18-Mar-26 A	24-Mar-26 A	86,709.19	86,709.19	86,709.19	100%	100%	16
BITU,INOUS BASE & WEARING COURSE		11	31-Mar-26	12-Apr-26	08-Mar-26 A	09-Mar-26 A	86,709.19	86,709.19	86,709.19	100%	100%	26
MKH2-02-003-EN-1950	Material Submittal for Bituminous B	5	31-Mar-26	05-Apr-26	08-Mar-26 A	09-Mar-26 A	0.00	0.00	0.00	100%	100%	20
MKH2-02-003-EN-1960	Material Approval for Bituminous B	6	06-Apr-26	12-Apr-26	08-Mar-26 A	09-Mar-26 A	86,709.19	86,709.19	86,709.19	100%	100%	26
PRE-CAST CONCRETE CURBS		11	31-Mar-26	12-Apr-26	29-Mar-26 A	29-Mar-26 A	86,709.19	86,709.19	86,709.19	100%	100%	12
MKH2-02-003-EN-1970	Material Submittal for Precast Conc	5	31-Mar-26	05-Apr-26	29-Mar-26 A	29-Mar-26 A	0.00	0.00	0.00	100%	100%	6
MKH2-02-003-EN-1980	Material Approval for Precast Conc	6	06-Apr-26	12-Apr-26	29-Mar-26 A	29-Mar-26 A	86,709.19	86,709.19	86,709.19	100%	100%	12
INTERLOCKING PAVING BLOCKS		11	31-Mar-26	12-Apr-26	29-Mar-26 A	29-Mar-26 A	86,709.19	86,709.19	86,709.19	100%	100%	12
MKH2-02-003-EN-1990	Material Submittal for Interlocking B	5	31-Mar-26	05-Apr-26	29-Mar-26 A	29-Mar-26 A	0.00	0.00	0.00	100%	100%	6
MKH2-02-003-EN-2000	Material Approval for Interlocking B	6	06-Apr-26	12-Apr-26	29-Mar-26 A	29-Mar-26 A	86,709.19	86,709.19	86,709.19	100%	100%	12
PAVEMENT MARKING		11	31-Mar-26	12-Apr-26	12-May-26 A	16-May-26 A	86,709.19	86,709.19	86,709.19	100%	100%	-29
MKH2-02-003-EN-2010	Material Submittal for Pavement Ma	5	31-Mar-26	05-Apr-26	12-May-26 A	16-May-26 A	0.00	0.00	0.00	100%	100%	-35
MKH2-02-003-EN-2020	Material Approval for Pavement Ma	6	06-Apr-26	12-Apr-26	12-May-26 A	16-May-26 A	86,709.19	86,709.19	86,709.19	100%	100%	-29
TRAFFIC SIGNS		11	31-Mar-26	12-Apr-26	22-Apr-26 A	28-Apr-26 A	86,709.19	86,709.19	86,709.19	100%	100%	-14
MKH2-02-003-EN-2030	Material Submittal for Traffic Signs	5	31-Mar-26	05-Apr-26	22-Apr-26 A	23-Apr-26 A	0.00	0.00	0.00	100%	100%	-16
MKH2-02-003-EN-2040	Material Approval for Traffic Signs	6	06-Apr-26	12-Apr-26	25-Apr-26 A	28-Apr-26 A	86,709.19	86,709.19	86,709.19	100%	100%	-14
ELECTRICAL NETWORK		41	31-Mar-26	12-Apr-26	28-Mar-26 A	29-Apr-26 A	606,964.35	606,964.35	606,964.35	100%	100%	-15
PIPE FOR DUCT		11	31-Mar-26	12-Apr-26	28-Mar-26 A	30-Mar-26 A	86,709.19	86,709.19	86,709.19	100%	100%	11
MKH2-02-003-EN-2050	Material Submittal for Pipe for the D	5	31-Mar-26	05-Apr-26	28-Mar-26 A	30-Mar-26 A	0.00	0.00	0.00	100%	100%	5
MKH2-02-003-EN-2060	Material Approval for Pipe for the D	6	06-Apr-26	12-Apr-26	28-Mar-26 A	30-Mar-26 A	86,709.19	86,709.19	86,709.19	100%	100%	11
LOW VOLTAGE CABLES		12	31-Mar-26	12-Apr-26	28-Mar-26 A	30-Mar-26 A	86,709.19	86,709.19	86,709.19	100%	100%	11
MKH2-02-003-EN-2070	Material Submittal for Low Voltage	5	31-Mar-26	05-Apr-26	28-Mar-26 A	28-Mar-26 A	0.00	0.00	0.00	100%	100%	7
MKH2-02-003-EN-2080	Material Approval for Low Voltage (	6	06-Apr-26	12-Apr-26	28-Mar-26 A	30-Mar-26 A	86,709.19	86,709.19	86,709.19	100%	100%	11
EARTHING SYSTEM		11	31-Mar-26	12-Apr-26	22-Apr-26 A	29-Apr-26 A	86,709.19	86,709.19	86,709.19	100%	100%	-15
MKH2-02-003-EN-2090	Material Submittal for Earthing Syst	5	31-Mar-26	05-Apr-26	22-Apr-26 A	23-Apr-26 A	0.00	0.00	0.00	100%	100%	-16
MKH2-02-003-EN-2100	Material Approval for Earthing Syst	6	06-Apr-26	12-Apr-26	25-Apr-26 A	29-Apr-26 A	86,709.19	86,709.19	86,709.19	100%	100%	-15
LOW VOLTAGE DISTRIBUTION PANNEL		11	31-Mar-26	12-Apr-26	18-Apr-26 A	21-Apr-26 A	86,709.19	86,709.19	86,709.19	100%	100%	-8
MKH2-02-003-EN-2110	Material Submittal for Distribution P	5	31-Mar-26	05-Apr-26	18-Apr-26 A	19-Apr-26 A	0.00	0.00	0.00	100%	100%	-12
MKH2-02-003-EN-2120	Material Approval for Distribution P	6	06-Apr-26	12-Apr-26	21-Apr-26 A	21-Apr-26 A	86,709.19	86,709.19	86,709.19	100%	100%	-8
LIGHTING POLES		36	31-Mar-26	12-Apr-26	04-Apr-26 A	09-Apr-26 A	86,709.19	86,709.19	86,709.19	100%	100%	2
MKH2-02-003-EN-2130	Material Submittal for Lighting poles	5	31-Mar-26	05-Apr-26	04-Apr-26 A	05-Apr-26 A	0.00	0.00	0.00	100%	100%	0
MKH2-02-003-EN-2140	Material Approval for Lighting poles	6	06-Apr-26	12-Apr-26	05-Apr-26 A	09-Apr-26 A	86,709.19	86,709.19	86,709.19	100%	100%	2
LIGHTINH PANNELS/FEEDER PILLERS		11	31-Mar-26	12-Apr-26	19-Apr-26 A	21-Apr-26 A	86,709.19	86,709.19	86,709.19	100%	100%	-8
MKH2-02-003-EN-2150	Material Submittal for Lighting pane	5	31-Mar-26	05-Apr-26	19-Apr-26 A	20-Apr-26 A	0.00	0.00	0.00	100%	100%	-13
MKH2-02-003-EN-2160	Material Approval for Lighting pane	6	06-Apr-26	12-Apr-26	21-Apr-26 A	21-Apr-26 A	86,709.19	86,709.19	86,709.19	100%	100%	-8
STREET LIGHTING LUMINAIRE		19	31-Mar-26	12-Apr-26	04-Apr-26 A	09-Apr-26 A	86,709.19	86,709.19	86,709.19	100%	100%	2
MKH2-02-003-EN-2170	Material Submittal for Lighting Lumi	5	31-Mar-26	05-Apr-26	04-Apr-26 A	05-Apr-26 A	0.00	0.00	0.00	100%	100%	0
MKH2-02-003-EN-2180	Material Approval for Lighting Lumi	6	06-Apr-26	12-Apr-26	05-Apr-26 A	09-Apr-26 A	86,709.19	86,709.19	86,709.19	100%	100%	2
OPPEN CHANNEL		22	31-Mar-26	14-Apr-26	03-Jun-26 A	06-Jun-26 A	173,418.39	173,418.39	173,418.39	100%	100%	-42
RIPRAP MATERIAL		22	31-Mar-26	12-Apr-26	03-Jun-26 A	06-Jun-26 A	86,709.19	86,709.19	86,709.19	100%	100%	-44
MKH2-02-003-EN-2190	Material Submittal for RIP-RAP Mat	5	31-Mar-26	05-Apr-26	03-Jun-26 A	04-Jun-26 A	0.00	0.00	0.00	100%	100%	-49
MKH2-02-003-EN-2200	Material Approval for RIP-RAP Mat	6	06-Apr-26	12-Apr-26	04-Jun-26 A	06-Jun-26 A	86,709.19	86,709.19	86,709.19	100%	100%	-44
ACCESSORIES FOR RIPRAP		13	31-Mar-26	14-Apr-26	03-Jun-26 A	06-Jun-26 A	86,709.19	86,709.19	86,709.19	100%	100%	-42
MKH2-02-003-EN-2210	Material Submittal for Accessories f	5	31-Mar-26	05-Apr-26	03-Jun-26 A	04-Jun-26 A	0.00	0.00	0.00	100%	100%	-49
MKH2-02-003-EN-2220	Material Approval for Accessories f	8	06-Apr-26	14-Apr-26	04-Jun-26 A	06-Jun-26 A	86,709.19	86,709.19	86,709.19	100%	100%	-42
PROCUREMENT		194	13-Apr-26	16-Aug-26	10-Mar-26 A	20-Dec-26	10,405,103.20	10,035,314.05	10,405,103.20	100%	96.45%	-107
SHORT LEAD ITEM		192	13-Apr-26	18-Jun-26	10-Mar-26 A	29-Nov-26	3,060,324.00	2,690,534.85	3,060,324.00	100%	87.92%	-139
ROAD WORKS-CIVIL		192	13-Apr-26	18-Jun-26	10-Mar-26 A	29-Nov-26	2,295,243.00	1,925,453.85	2,295,243.00	100%	83.89%	-139
STEEL REINFORCEMENT		55	13-Apr-26	18-Jun-26	10-Mar-26 A	25-Jun-26 A	255,027.00	255,027.00	255,027.00	100%	100%	-6

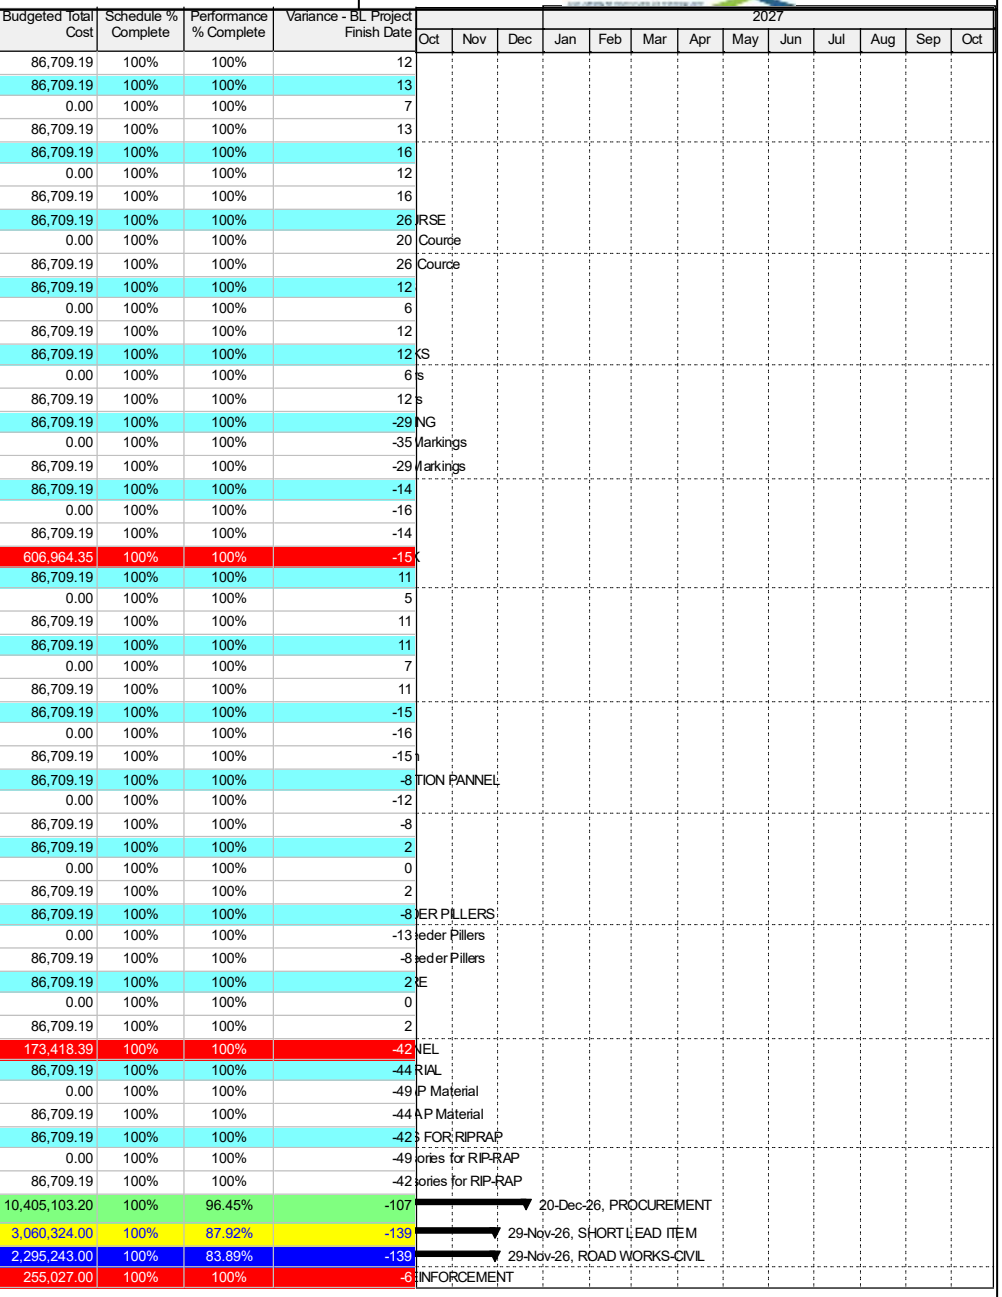

Actual Work
Remaining Work
Critical Remaining Work
Milestone


Date	Revision	Checked	Approved

egis ENJAZCO

MKH2-02-003 - Completion of Infrastructure Works at the Second Industrial City in Makkah UP 31
WBS L5

MODON مدن


Activity ID	Activity Name	Original Duration	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Schedule % Complete	Performance % Complete	Variance - BL Project Finish Date
MKH2-02-003-PR-1000	PO for Steel Reinforcement	9	13-Apr-26	22-Apr-26	10-Mar-26 A	11-Mar-26 A	0.00	0.00	0.00	100%	100%	33
MKH2-02-003-PR-1010	Material Fabrication for Steel Reinfc	16	23-Apr-26	11-May-26	12-Mar-26 A	15-Mar-26 A	0.00	0.00	0.00	100%	100%	46
MKH2-02-003-PR-1020	Material Delivery for 1st lot of Steel	15	12-May-26	01-Jun-26	18-Mar-26 A	25-Mar-26 A	127,513.50	127,513.50	127,513.50	100%	100%	55
MKH2-02-003-PR-1030	Material Delivery for 2nd lot of Stee	15	02-Jun-26	18-Jun-26	16-May-26 A	25-Jun-26 A	127,513.50	127,513.50	127,513.50	100%	100%	-6
READY MIX CONCRETE		35	13-Apr-26	23-May-26	07-Apr-26 A	22-Aug-26 A	255,027.00	255,027.00	255,027.00	100%	100%	-75
MKH2-02-003-PR-1040	PO for Ready Mixed Concrete	9	13-Apr-26	22-Apr-26	07-Apr-26 A	07-Apr-26 A	0.00	0.00	0.00	100%	100%	13
MKH2-02-003-PR-1050	Material Delivery for 1st lot of Ready	26	23-Apr-26	23-May-26	07-Apr-26 A	22-Aug-26 A	255,027.00	255,027.00	255,027.00	100%	100%	-75
WATER PROOFING		48	13-Apr-26	10-Jun-26	08-Apr-26 A	11-Jun-26 A	255,027.00	255,027.00	255,027.00	100%	100%	-1
MKH2-02-003-PR-1060	PO for Water Proofing	6	13-Apr-26	19-Apr-26	08-Apr-26 A	08-Apr-26 A	0.00	0.00	0.00	100%	100%	9
MKH2-02-003-PR-1070	Material Fabrication for Water Proof	20	20-Apr-26	12-May-26	09-Apr-26 A	10-Jun-26 A	0.00	0.00	0.00	100%	100%	-22
MKH2-02-003-PR-1080	Material Delivery for 1st lot of Water	22	13-May-26	10-Jun-26	11-Apr-26 A	11-Jun-26 A	255,027.00	255,027.00	255,027.00	100%	100%	-1
AGGREGATE BASE COURSE		80	13-Apr-26	06-Jun-26	11-Mar-26 A	19-Aug-26 A	255,027.00	255,027.00	255,027.00	100%	100%	-64
MKH2-02-003-PR-1090	PO for Aggregate Base Course	4	13-Apr-26	16-Apr-26	11-Mar-26 A	12-Mar-26 A	0.00	0.00	0.00	100%	100%	27
MKH2-02-003-PR-1100	Material Delivery for 1st lot of Aggre	20	18-Apr-26	10-May-26	14-Mar-26 A	10-Jun-26 A	127,513.50	127,513.50	127,513.50	100%	100%	-24
MKH2-02-003-PR-1110	Material Delivery for 2nd lot of Aggr	20	11-May-26	06-Jun-26	11-Jun-26 A	19-Aug-26 A	127,513.50	127,513.50	127,513.50	100%	100%	-64
BITUMINOUS BASE & WEARING COURSE		29	13-Apr-26	16-May-26	08-Apr-26 A	01-Nov-26	255,027.00	191,270.25	255,027.00	100%	75%	-141
MKH2-02-003-PR-1120	PO for Bituminous Base & Wearing	4	13-Apr-26	16-Apr-26	08-Apr-26 A	08-Apr-26 A	0.00	0.00	0.00	100%	100%	7
MKH2-02-003-PR-1130	Material Delivery for 1st lot to the Si	25	18-Apr-26	16-May-26	08-Apr-26 A	01-Nov-26	255,027.00	191,270.25	255,027.00	100%	75%	-141
PRE-CAST CONCRETE CURBS		72	13-Apr-26	16-Jun-26	20-Apr-26 A	08-Aug-26 A	255,027.00	255,027.00	255,027.00	100%	100%	-45
MKH2-02-003-PR-1140	PO for Precast Concrete curb	4	13-Apr-26	16-Apr-26	20-Apr-26 A	21-Apr-26 A	0.00	0.00	0.00	100%	100%	-4
MKH2-02-003-PR-1150	Material Fabrication for Precast Con	24	18-Apr-26	14-May-26	22-Apr-26 A	23-Apr-26 A	0.00	0.00	0.00	100%	100%	18
MKH2-02-003-PR-1160	Material Delivery for 1st lot of Preca	25	16-May-26	16-Jun-26	25-Apr-26 A	08-Aug-26 A	255,027.00	255,027.00	255,027.00	100%	100%	-45
INTERLOCKING PAVING BLOCKS		113	13-Apr-26	14-Jun-26	16-May-26 A	26-Nov-26	255,027.00	204,021.60	255,027.00	100%	80%	-141
MKH2-02-003-PR-1170	PO for Interlocking Block Pavers	5	13-Apr-26	18-Apr-26	16-May-26 A	17-May-26 A	0.00	0.00	0.00	100%	100%	-25
MKH2-02-003-PR-1180	Material Fabrication for Interlocking	24	19-Apr-26	16-May-26	17-May-26 A	18-May-26 A	0.00	0.00	0.00	100%	100%	-2
MKH2-02-003-PR-1190	Material Delivery for 1st lot of Interlo	22	17-May-26	14-Jun-26	15-Jul-26 A	26-Nov-26	255,027.00	204,021.60	255,027.00	100%	80%	-141
PAVEMENT MARKING		57	13-Apr-26	14-Jun-26	16-Sep-26 A	29-Nov-26	255,027.00	0.00	255,027.00	100%	0%	-143
MKH2-02-003-PR-1200	PO for Pavement Markings	5	13-Apr-26	18-Apr-26	16-Sep-26 A	19-Sep-26 A	0.00	0.00	0.00	100%	100%	-129
MKH2-02-003-PR-1210	Material Fabrication for Pavement M	24	19-Apr-26	16-May-26	07-Oct-26	03-Nov-26	0.00	0.00	0.00	100%	0%	-143
MKH2-02-003-PR-1220	Material Delivery for 1st lot of Paver	22	17-May-26	14-Jun-26	04-Nov-26	29-Nov-26	255,027.00	0.00	255,027.00	100%	0%	-143
TRAFFIC SIGNS		60	13-Apr-26	06-Jun-26	29-Apr-26 A	01-Jul-26 A	255,027.00	255,027.00	255,027.00	100%	100%	-21
MKH2-02-003-PR-1230	PO for Traffic Signs	6	13-Apr-26	19-Apr-26	29-Apr-26 A	30-Apr-26 A	0.00	0.00	0.00	100%	100%	-10
MKH2-02-003-PR-1240	Material Fabrication for Traffic Signs	24	20-Apr-26	17-May-26	02-May-26 A	10-Jun-26 A	0.00	0.00	0.00	100%	100%	-18
MKH2-02-003-PR-1250	Material Delivery for 1st lot of Traffic	14	18-May-26	06-Jun-26	10-Jun-26 A	01-Jul-26 A	255,027.00	255,027.00	255,027.00	100%	100%	-21
ELECTRICAL NETWORK		87	13-Apr-26	18-Jun-26	01-Apr-26 A	01-Jul-26 A	510,054.00	510,054.00	510,054.00	100%	100%	-11
PIPE FOR THE DUCTS		55	13-Apr-26	18-Jun-26	01-Apr-26 A	18-Jun-26 A	255,027.00	255,027.00	255,027.00	100%	100%	0
MKH2-02-003-PR-1260	PO for Pipe for Duct	11	13-Apr-26	25-Apr-26	01-Apr-26 A	01-Apr-26 A	0.00	0.00	0.00	100%	100%	20
MKH2-02-003-PR-1270	Material Fabrication for Pipe for Duc	24	26-Apr-26	23-May-26	01-Apr-26 A	08-Jun-26 A	0.00	0.00	0.00	100%	100%	-11
MKH2-02-003-PR-1280	Material Delivery for 1st lot of Pipe f	20	24-May-26	18-Jun-26	08-Jun-26 A	18-Jun-26 A	255,027.00	255,027.00	255,027.00	100%	100%	0
EARTHING SYSTEM		74	13-Apr-26	18-Jun-26	29-Apr-26 A	01-Jul-26 A	255,027.00	255,027.00	255,027.00	100%	100%	-11
MKH2-02-003-PR-1290	PO for Earthing System	9	13-Apr-26	22-Apr-26	29-Apr-26 A	30-Apr-26 A	0.00	0.00	0.00	100%	100%	-7
MKH2-02-003-PR-1300	Material Fabrication for Earthing Sy	24	23-Apr-26	20-May-26	02-May-26 A	17-Jun-26 A	0.00	0.00	0.00	100%	100%	-21
MKH2-02-003-PR-1310	Material Delivery for 1st lot of Earthi	22	21-May-26	18-Jun-26	18-Jun-26 A	01-Jul-26 A	255,027.00	255,027.00	255,027.00	100%	100%	-11
OPEN CHANNEL		22	15-Apr-26	10-May-26	10-Jun-26 A	08-Sep-26 A	255,027.00	255,027.00	255,027.00	100%	100%	-101
MKH2-02-003-PR-1320	PO for RIP-RAP Material & Its Acess	4	15-Apr-26	19-Apr-26	10-Jun-26 A	11-Jun-26 A	0.00	0.00	0.00	100%	100%	-43
MKH2-02-003-PR-1330	Material Delivery for RIP-RAP Mater	18	20-Apr-26	10-May-26	17-Jun-26 A	08-Sep-26 A	255,027.00	255,027.00	255,027.00	100%	100%	-101
LONG LEAD ITEM		170	13-Apr-26	16-Aug-26	25-Apr-26 A	20-Dec-26	7,344,779.20	7,344,779.20	7,344,779.20	100%	100%	-107
ELECTRICAL POWER		109	13-Apr-26	02-Aug-26	16-May-26 A	09-Dec-26	2,937,911.68	2,937,911.68	2,937,911.68	100%	100%	-110
LV-CABLES		87	13-Apr-26	25-Jul-26	16-May-26 A	08-Dec-26	1,468,955.84	1,468,955.84	1,468,955.84	100%	100%	-116
MKH2-02-003-PR-1340	PO for Low Voltage Cables	6	13-Apr-26	19-Apr-26	16-May-26 A	17-May-26 A	0.00	0.00	0.00	100%	100%	-24
MKH2-02-003-PR-1350	Material Fabrication for Low Voltage	9	20-Apr-26	29-Apr-26	17-May-26 A	18-May-26 A	0.00	0.00	0.00	100%	100%	-16
MKH2-02-003-PR-1360	Material Fabrication for Low Voltage	20	30-Apr-26	23-May-26	17-May-26 A	18-May-26 A	0.00	0.00	0.00	100%	100%	4
MKH2-02-003-PR-1370	Material Fabrication for Low Voltage	20	24-May-26	18-Jun-26	17-May-26 A	18-May-26 A	0.00	0.00	0.00	100%	100%	24
MKH2-02-003-PR-1380	6/2	22	20-Jun-26	14-Jul-26	20-May-26 A	25-Jun-26 A	1,468,955.84	1,468,955.84	1,468,955.84	100%	100%	17
MKH2-02-003-PR-1390	Staging Time for Low Voltage Cable	9	15-Jul-26	25-Jul-26	20-May-26 A	08-Dec-26	0.00	0.00	0.00	100%	60%	-116

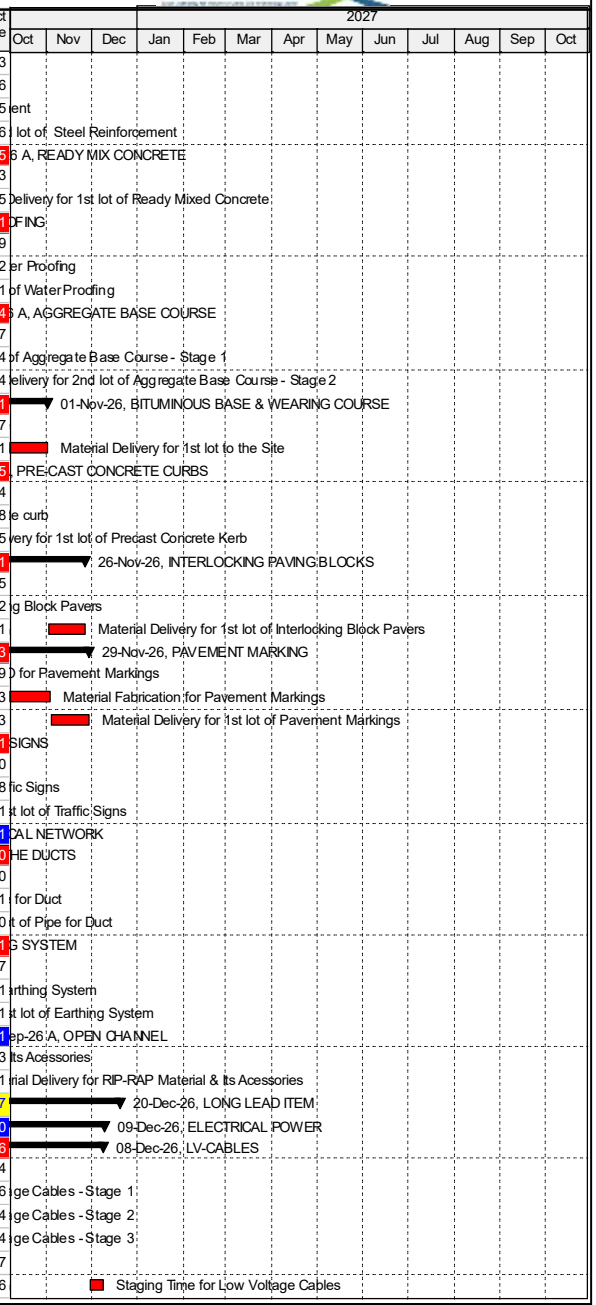

Actual Work
Remaining Work
Critical Remaining Work
Milestone

Date	Revision	Checked	Approved


Activity ID	Activity Name	Original Duration	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Schedule % Complete	Performance % Complete	Variance - BL Project Finish Date
LV-DISTRIBUTION PANNELS		90	13-Apr-26	02-Aug-26	25-May-26 A	09-Dec-26	1,468,955.84	1,468,955.84	1,468,955.84	100%	100%	-110
MKH2-02-003-PR-1400	PO for Low Voltage Distribution Par	5	13-Apr-26	18-Apr-26	25-May-26 A	26-May-26 A	0.00	0.00	0.00	100%	100%	-32
MKH2-02-003-PR-1410	Material Fabrication for Low Voltage	17	19-Apr-26	07-May-26	10-Jun-26 A	11-Jun-26 A	0.00	0.00	0.00	100%	100%	-27
MKH2-02-003-PR-1420	Material Fabrication for Low Voltage	16	09-May-26	30-May-26	13-Jun-26 A	14-Jun-26 A	0.00	0.00	0.00	100%	100%	-13
MKH2-02-003-PR-1430	Material Fabrication for Low Voltage	16	31-May-26	17-Jun-26	30-Jun-26 A	01-Jul-26 A	0.00	0.00	0.00	100%	100%	-12
MKH2-02-003-PR-1440	Material Delivery for Low Voltage Di	22	18-Jun-26	13-Jul-26	02-Jul-26 A	18-Jul-26 A	734,477.92	734,477.92	734,477.92	100%	100%	-4
MKH2-02-003-PR-1450	Material Delivery for Low Voltage Di	8	14-Jul-26	22-Jul-26	18-Jul-26 A	29-Aug-26 A	734,477.92	734,477.92	734,477.92	100%	100%	-32
MKH2-02-003-PR-1460	Staging Time for LV Distribution par	9	23-Jul-26	02-Aug-26	18-Jul-26 A	09-Dec-26	0.00	0.00	0.00	100%	0%	-110
STREET LIGHTING		170	13-Apr-26	16-Aug-26	25-Apr-26 A	20-Dec-26	4,406,867.52	4,406,867.52	4,406,867.52	100%	100%	-107
POLES		107	13-Apr-26	02-Aug-26	25-Apr-26 A	15-Oct-26	1,468,955.84	1,468,955.84	1,468,955.84	100%	100%	-63
MKH2-02-003-PR-1470	PO for Lighting poles single arm & d	4	13-Apr-26	16-Apr-26	25-Apr-26 A	26-Apr-26 A	0.00	0.00	0.00	100%	100%	-8
MKH2-02-003-PR-1480	Material Fabrication for Lighting pol	9	18-Apr-26	27-Apr-26	27-Apr-26 A	30-Apr-26 A	0.00	0.00	0.00	100%	100%	-3
MKH2-02-003-PR-1490	Material Fabrication for Lighting pol	20	28-Apr-26	20-May-26	04-Jun-26 A	06-Jun-26 A	0.00	0.00	0.00	100%	100%	-11
MKH2-02-003-PR-1500	Material Fabrication for Lighting pol	20	21-May-26	16-Jun-26	08-Jun-26 A	09-Jun-26 A	0.00	0.00	0.00	100%	100%	6
MKH2-02-003-PR-1510	Material Delivery for Lighting poles '	22	17-Jun-26	12-Jul-26	10-Jun-26 A	18-Jun-26 A	734,477.92	734,477.92	734,477.92	100%	100%	21
MKH2-02-003-PR-1520	Material Delivery for Lighting poles 2	9	13-Jul-26	22-Jul-26	18-Jun-26 A	25-Jun-26 A	734,477.92	734,477.92	734,477.92	100%	100%	24
MKH2-02-003-PR-1530	Staging Time for Street Light poles	9	23-Jul-26	02-Aug-26	10-Jun-26 A	15-Oct-26	0.00	0.00	0.00	100%	0%	-63
PANNELS & FEEDER PILLERS		143	13-Apr-26	12-Aug-26	25-May-26 A	20-Dec-26	1,468,955.84	1,468,955.84	1,468,955.84	100%	100%	-110
MKH2-02-003-PR-1540	PO for Lighting Panels/Feeder Piller	3	13-Apr-26	15-Apr-26	25-May-26 A	26-May-26 A	0.00	0.00	0.00	100%	100%	-34
MKH2-02-003-PR-1550	Material Fabrication for Lighting Par	20	16-Apr-26	09-May-26	10-Jun-26 A	11-Jun-26 A	0.00	0.00	0.00	100%	100%	-26
MKH2-02-003-PR-1560	Material Fabrication for Lighting Par	20	10-May-26	04-Jun-26	13-Aug-26 A	15-Aug-26 A	0.00	0.00	0.00	100%	100%	-61
MKH2-02-003-PR-1570	Material Fabrication for Lighting Par	20	06-Jun-26	28-Jun-26	15-Aug-26 A	16-Aug-26 A	0.00	0.00	0.00	100%	100%	-42
MKH2-02-003-PR-1580	Material Delivery for Lighting Panels	22	29-Jun-26	23-Jul-26	20-Aug-26 A	29-Aug-26 A	734,477.92	734,477.92	734,477.92	100%	100%	-31
MKH2-02-003-PR-1590	Material Delivery for Lighting Panels	8	25-Jul-26	02-Aug-26	26-Aug-26 A	29-Aug-26 A	734,477.92	734,477.92	734,477.92	100%	100%	-23
MKH2-02-003-PR-1600	Staging Time for Lighting Panels/Fe	9	03-Aug-26	12-Aug-26	20-Aug-26 A	20-Dec-26	0.00	0.00	0.00	100%	0%	-110
LUMINAIRE		126	13-Apr-26	16-Aug-26	25-Apr-26 A	17-Dec-26	1,468,955.84	1,468,955.84	1,468,955.84	100%	100%	-105
MKH2-02-003-PR-1610	PO for Street Lighting Luminaire	6	13-Apr-26	19-Apr-26	25-Apr-26 A	26-Apr-26 A	0.00	0.00	0.00	100%	100%	-6
MKH2-02-003-PR-1620	Material Fabrication for Street Lighti	20	20-Apr-26	12-May-26	27-Apr-26 A	30-Apr-26 A	0.00	0.00	0.00	100%	100%	10
MKH2-02-003-PR-1630	Material Fabrication for Street Lighti	20	13-May-26	08-Jun-26	06-Jun-26 A	07-Jun-26 A	0.00	0.00	0.00	100%	100%	1
MKH2-02-003-PR-1640	Material Fabrication for Street Lighti	20	09-Jun-26	01-Jul-26	08-Jun-26 A	09-Jun-26 A	0.00	0.00	0.00	100%	100%	19
MKH2-02-003-PR-1650	Material Delivery for Street Lighting	22	02-Jul-26	27-Jul-26	10-Jun-26 A	18-Jun-26 A	734,477.92	734,477.92	734,477.92	100%	100%	33
MKH2-02-003-PR-1660	Material Delivery for Street Lighting	8	28-Jul-26	05-Aug-26	20-Jun-26 A	25-Jun-26 A	734,477.92	734,477.92	734,477.92	100%	100%	36
MKH2-02-003-PR-1670	Staging Time for Street Lighting Lur	9	06-Aug-26	16-Aug-26	10-Jun-26 A	17-Dec-26	0.00	0.00	0.00	100%	0%	-105
CONSTRUCTION PHASE		396	26-Mar-26	14-Jun-27	18-Feb-26 A	26-Jul-27	16,131,419.60	27,587,209.47	34,857,095.72	46.28%	79.14%	-36
ROADS		373	26-Mar-26	07-Jun-27	18-Feb-26 A	07-Jul-27	13,850,467.78	18,100,842.10	24,376,620.72	56.82%	74.25%	-26
ARTERIAL-03 (2+510 to 4+267.54)		295	26-Mar-26	15-Mar-27	18-Feb-26 A	03-Mar-27	8,099,706.52	10,726,046.54	11,737,666.14	69.01%	91.38%	7
Box Culvert - 1		105	26-Mar-26	05-Jul-26	04-Mar-26 A	22-Aug-26 A	2,986,578.60	2,986,578.60	2,986,578.60	100%	100%	-41
MKH2-02-003-CN-2030	Excavation in (all types of soil) inclu	21	26-Mar-26	19-Apr-26	04-Mar-26 A	30-Apr-26 A	255,792.60	255,792.60	255,792.60	100%	100%	-10
MKH2-02-003-CN-2050	Plain Concrete for box culvert [Roac	21	20-Apr-26	13-May-26	07-May-26 A	09-May-26 A	61,506.00	61,506.00	61,506.00	100%	100%	4
MKH2-02-003-CN-2070	Steel Reinforcement for box culverts	21	14-May-26	10-Jun-26	13-May-26 A	21-Aug-26 A	1,150,926.00	1,150,926.00	1,150,926.00	100%	100%	-61
MKH2-02-003-CN-2080	Concrete for box culvert including bi	21	11-Jun-26	05-Jul-26	03-Jun-26 A	22-Aug-26 A	1,518,354.00	1,518,354.00	1,518,354.00	100%	100%	-41
ARTERIAL-03-ROAD		289	20-Apr-26	15-Mar-27	18-Feb-26 A	03-Mar-27	5,113,127.92	7,739,467.94	8,751,087.54	58.43%	88.44%	7
ROADS & ROUNDABOUT		289	20-Apr-26	15-Mar-27	18-Feb-26 A	03-Mar-27	4,881,885.55	6,550,432.34	7,533,911.94	64.8%	86.95%	7
EARTHWORKS & SITE GRADING		103	20-Apr-26	08-Aug-26	18-Feb-26 A	18-Apr-26 A	3,259,234.89	3,259,234.89	3,259,234.89	100%	100%	93
MKH2-02-003-CN-1050	Roadway Excavation for cuttings AF	15	20-Apr-26	06-May-26	18-Feb-26 A	05-Mar-26 A	537,723.78	537,723.78	537,723.78	100%	100%	51
MKH2-02-003-CN-1060	Roadway Excavation for cuttings AF	15	07-May-26	24-May-26	05-Mar-26 A	10-Mar-26 A	537,724.04	537,724.04	537,724.04	100%	100%	61
MKH2-02-003-CN-1070	Roadway Excavation for cuttings AF	15	25-May-26	14-Jun-26	10-Mar-26 A	09-Apr-26 A	537,724.04	537,724.04	537,724.04	100%	100%	53
MKH2-02-003-CN-1080	Roadway Excavation for cuttings AF	15	17-Jun-26	04-Jul-26	09-Apr-26 A	16-Apr-26 A	537,724.04	537,724.04	537,724.04	100%	100%	64
MKH2-02-003-CN-1150	Embankments -ARTERIAL-03	15	05-Jul-26	21-Jul-26	19-Feb-26 A	09-Apr-26 A	910,071.24	910,071.24	910,071.24	100%	100%	85
MKH2-02-003-CN-1200	Subgrade for ARTERIAL-03	15	22-Jul-26	08-Aug-26	10-Mar-26 A	18-Apr-26 A	198,267.74	198,267.74	198,267.74	100%	100%	93
ASPHALT WORKS		142	09-Aug-26	07-Jan-27	14-Mar-26 A	07-Feb-27	1,622,650.67	1,983,200.00	2,854,052.60	56.85%	69.49%	-26
MKH2-02-003-CN-1250	Aggregate base course at ARTERIA	20	09-Aug-26	31-Aug-26	14-Mar-26 A	21-Apr-26 A	300,428.00	300,428.00	300,428.00	100%	100%	110
MKH2-02-003-CN-1300	Prime Coat (MC1) ARTERIAL-03	14	01-Sep-26	16-Sep-26	08-Apr-26 A	30-Apr-26 A	168,464.80	168,464.80	168,464.80	100%	100%	116
MKH2-02-003-CN-1350	Bituminous base course for ARTERI	21	17-Sep-26	12-Oct-26	09-Apr-26 A	03-May-26 A	1,153,757.87	1,514,307.20	1,514,307.20	76.19%	100%	135

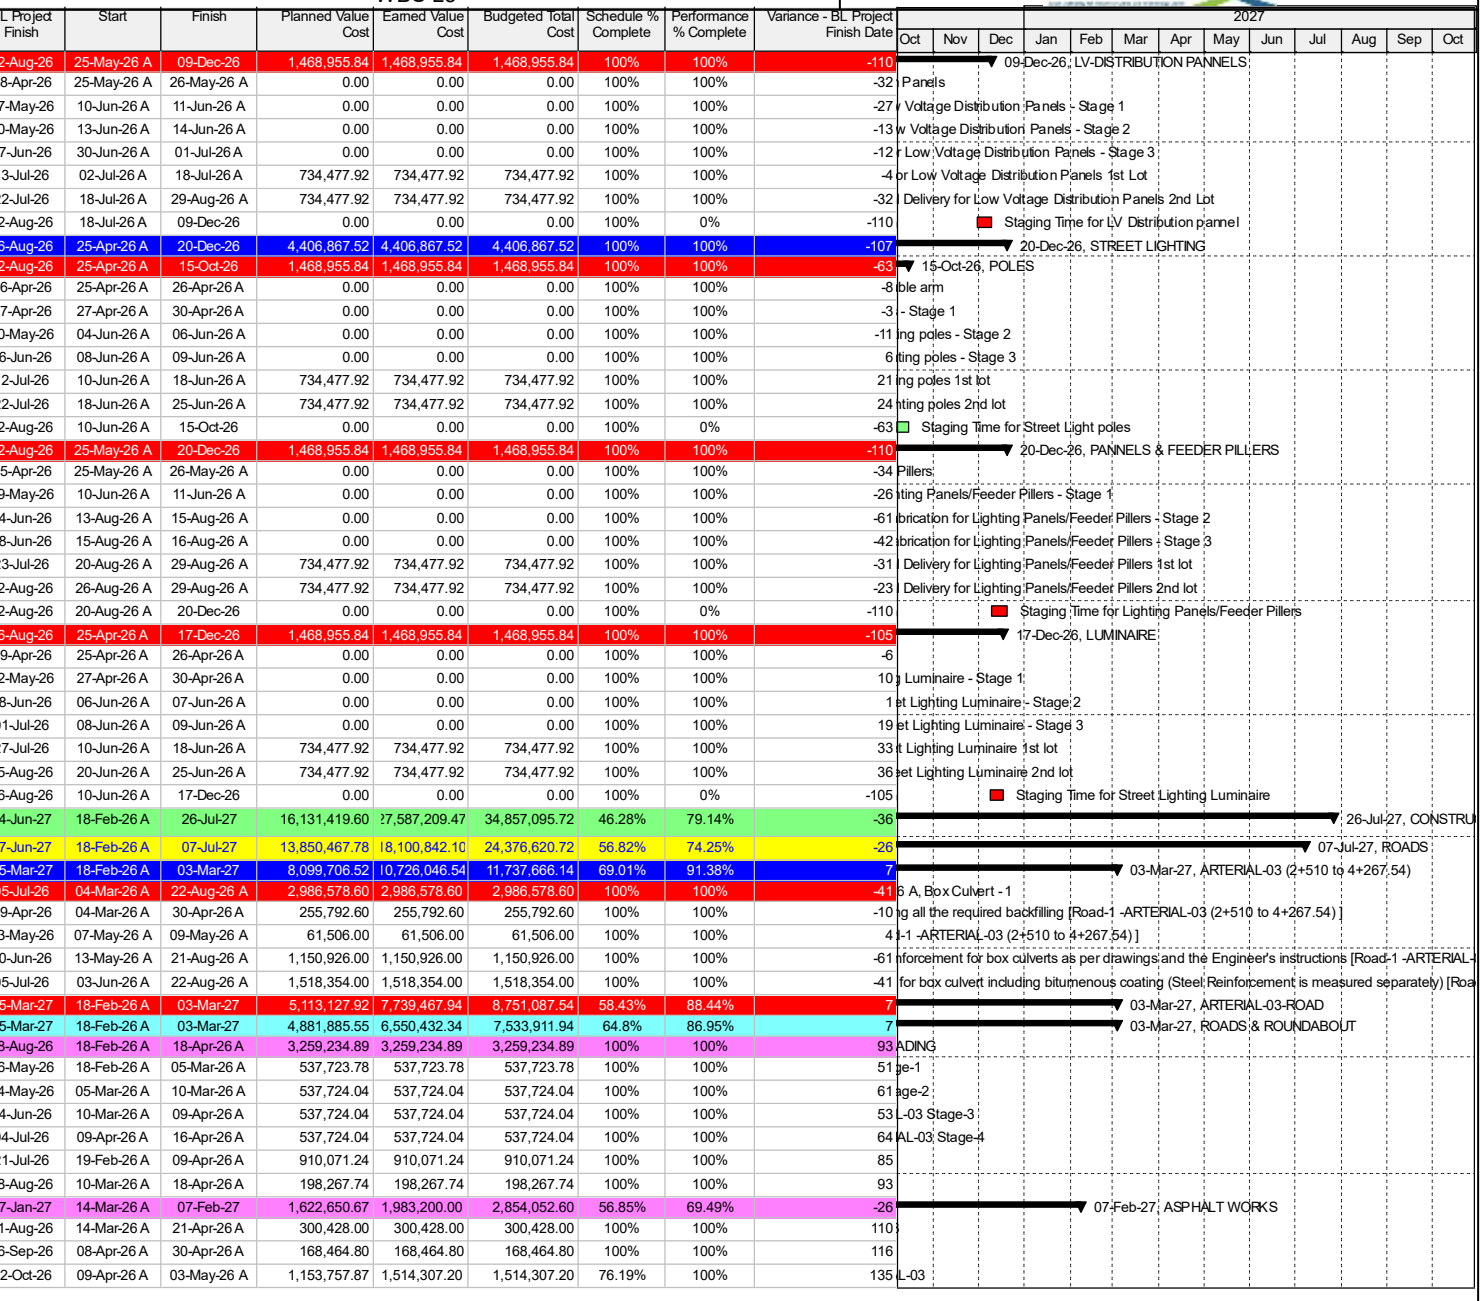

Actual Work | Critical Remaining Work | Remaining Work | Milestone

Date	Revision	Checked	Approved


Activity ID	Activity Name	Original Duration	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Schedule % Complete	Performance % Complete	Variance - BL Project Finish Date
MKH2-02-003-CN-1400	Tack coat at ARTERIAL-03	21	21-Nov-26	14-Dec-26	21-Dec-26	13-Jan-27	0.00	0.00	87,046.40	0%	0%	-26
MKH2-02-003-CN-1450	Bituminous concrete wearing course	21	15-Dec-26	07-Jan-27	14-Jan-27	07-Feb-27	0.00	0.00	783,806.20	0%	0%	-26
FINISHING WORKS		59	09-Jan-27	15-Mar-27	25-Apr-26 A	03-Mar-27	0.00	1,307,997.45	1,420,624.45	0%	92.07%	7
MKH2-02-003-CN-1500	Installation of Precast Concrete curb	16	09-Jan-27	26-Jan-27	25-Apr-26 A	18-Aug-26 A	0.00	523,594.95	523,594.95	0%	100%	137
MKH2-02-003-CN-1540	60mm thick - Interlocking block pave	17	27-Jan-27	15-Feb-27	30-Jul-26 A	19-Sep-26 A	0.00	784,402.50	784,402.50	0%	100%	127
MKH2-02-003-CN-1580	Pavement markings [Road-1 -ARTE	10	16-Feb-27	28-Feb-27	08-Feb-27	18-Feb-27	0.00	0.00	89,847.00	0%	0%	7
MKH2-02-003-CN-1630	Installation of Traffic Signs [Road-1 -	10	01-Mar-27	15-Mar-27	20-Feb-27	03-Mar-27	0.00	0.00	22,780.00	0%	0%	7
ELECTRICAL		142	09-Aug-26	14-Jan-27	01-Apr-26 A	03-Jan-27	231,242.36	1,189,035.60	1,217,175.60	19%	97.69%	10
LV NETWORKS		132	09-Aug-26	26-Nov-26	01-Apr-26 A	03-Jan-27	49,228.25	154,502.00	174,602.00	28.19%	88.49%	-32
MKH2-02-003-CN-1890	Installation of Road Crossing Ducts	14	09-Aug-26	24-Aug-26	01-Apr-26 A	23-Apr-26 A	7,236.00	7,236.00	7,236.00	100%	100%	102
MKH2-02-003-CN-1920	Installation of Road Crossing Ducts	15	25-Aug-26	10-Sep-26	09-Apr-26 A	25-Apr-26 A	13,936.00	13,936.00	13,936.00	100%	100%	116
MKH2-02-003-CN-1940	Installation of Road Crossing Ducts	14	12-Sep-26	28-Sep-26	10-Jun-26 A	11-Jun-26 A	8,710.00	8,710.00	8,710.00	100%	100%	92
MKH2-02-003-CN-1950	Drawpit with medium duty steel cov	16	29-Sep-26	17-Oct-26	03-Sep-26 A	23-Sep-26 A	19,346.25	44,220.00	44,220.00	43.75%	100%	20
MKH2-02-003-CN-1970	Drawpit with medium duty steel cov	15	18-Oct-26	03-Nov-26	05-Sep-26 A	08-Sep-26 A	0.00	24,120.00	24,120.00	0%	100%	47
MKH2-02-003-CN-2000	Feeder pillars [Road-1 -ARTERIAL-(	12	04-Nov-26	17-Nov-26	21-Dec-26	03-Jan-27	0.00	0.00	20,100.00	0%	0%	-40
MKH2-02-003-CN-2010	Street Lighting panels [Road-1 -ART	8	18-Nov-26	26-Nov-26	24-Sep-26 A	26-Sep-26 A	0.00	56,280.00	56,280.00	0%	100%	53
LV CABLES		99	25-Aug-26	19-Nov-26	25-Jun-26 A	20-Aug-26 A	182,014.11	424,699.60	424,699.60	42.86%	100%	77
MKH2-02-003-CN-1690	Installation of Low Voltage Cables -	21	25-Aug-26	17-Sep-26	25-Jun-26 A	16-Jul-26 A	106,174.90	106,174.90	106,174.90	100%	100%	54
MKH2-02-003-CN-1700	Installation of Low Voltage Cables -	21	19-Sep-26	13-Oct-26	06-Aug-26 A	08-Aug-26 A	75,839.21	106,174.90	106,174.90	71.43%	100%	56
MKH2-02-003-CN-1710	Installation of Low Voltage Cables -	16	14-Oct-26	01-Nov-26	08-Aug-26 A	09-Aug-26 A	0.00	106,174.90	106,174.90	0%	100%	71
MKH2-02-003-CN-1720	Installation of Low Voltage Cables -	16	02-Nov-26	19-Nov-26	17-Aug-26 A	20-Aug-26 A	0.00	106,174.90	106,174.90	0%	100%	77
STREET LIGHTING NETWORK INCLUDING ALL		36	21-Nov-26	31-Dec-26	10-Jun-26 A	18-Jul-26 A	0.00	607,824.00	607,824.00	0%	100%	142
MKH2-02-003-CN-1770	Installation of Lighting Poles 2-Arms	18	21-Nov-26	10-Dec-26	10-Jun-26 A	18-Jul-26 A	0.00	434,160.00	434,160.00	0%	100%	124
MKH2-02-003-CN-1810	Installation of Lighting Luminaires fo	18	12-Dec-26	31-Dec-26	14-Jun-26 A	18-Jul-26 A	0.00	173,664.00	173,664.00	0%	100%	142
EARTHING		12	02-Jan-27	14-Jan-27	30-Sep-26 A	29-Dec-26	0.00	2,010.00	10,050.00	0%	20%	14
MKH2-02-003-CN-1850	Installation of Earthing System for A	12	02-Jan-27	14-Jan-27	30-Sep-26 A	29-Dec-26	0.00	2,010.00	10,050.00	0%	20%	14
ARTERIAL-04 (0+000 to 1+0.83)		338	25-May-26	06-May-27	10-Mar-26 A	24-May-27	3,952,729.50	6,228,556.14	7,559,557.30	52.29%	82.39%	-12
Box Culvert - 2		134	25-May-26	31-Aug-26	25-Mar-26 A	05-Aug-26 A	973,362.60	973,362.60	973,362.60	100%	100%	22
MKH2-02-003-CN-2040	Excavation in (all types of soil) inclu	21	25-May-26	21-Jun-26	25-Mar-26 A	31-Mar-26 A	83,535.60	83,535.60	83,535.60	100%	100%	67
MKH2-02-003-CN-2060	Plain Concrete for box culvert [Roac	20	22-Jun-26	14-Jul-26	07-Apr-26 A	07-Apr-26 A	19,899.00	19,899.00	19,899.00	100%	100%	81
MKH2-02-003-CN-2090	Steel Reinforcement for box culverts	21	15-Jul-26	08-Aug-26	09-Apr-26 A	05-Aug-26 A	374,262.00	374,262.00	374,262.00	100%	100%	2
MKH2-02-003-CN-2120	Concrete for box culvert including bi	20	09-Aug-26	31-Aug-26	28-Apr-26 A	03-Aug-26 A	495,666.00	495,666.00	495,666.00	100%	100%	24
ARTERIAL-04-ROAD		304	22-Jun-26	06-May-27	10-Mar-26 A	24-May-27	2,979,366.90	5,255,193.54	6,586,194.70	45.24%	79.79%	-12
ROADS		254	22-Jun-26	14-Mar-27	10-Mar-26 A	13-Apr-27	2,970,408.04	4,675,406.36	5,938,291.30	50.02%	78.73%	-26
EARTHWORKS & SITE GRADING		68	22-Jun-26	20-Sep-26	10-Mar-26 A	26-Oct-26	2,763,436.67	2,706,618.23	2,763,436.67	100%	97.94%	-30
MKH2-02-003-CN-1090	Roadway Excavation for cuttings AF	20	22-Jun-26	14-Jul-26	10-Mar-26 A	16-May-26 A	911,848.83	911,848.83	911,848.83	100%	100%	49
MKH2-02-003-CN-1100	Roadway Excavation for cuttings AF	20	15-Jul-26	06-Aug-26	20-May-26 A	15-Oct-26	911,848.83	893,611.85	911,848.83	100%	98%	-59
MKH2-02-003-CN-1160	Embankments -ARTERIAL-04	18	08-Aug-26	27-Aug-26	20-Apr-26 A	26-Oct-26	771,629.31	733,047.85	771,629.31	100%	95%	-50
MKH2-02-003-CN-1210	Subgrade for ARTERIAL-04	20	29-Aug-26	20-Sep-26	25-Apr-26 A	29-Jul-26 A	168,109.70	168,109.70	168,109.70	100%	100%	45
ASPHALT WORKS		169	21-Sep-26	23-Jan-27	20-May-26 A	23-Feb-27	206,971.38	1,681,619.60	2,420,348.20	8.55%	69.48%	-26
MKH2-02-003-CN-1260	Aggregate base course at ARTERIA	16	21-Sep-26	10-Oct-26	20-May-26 A	05-Aug-26 A	206,971.38	254,734.00	254,734.00	81.25%	100%	55
MKH2-02-003-CN-1310	Prime Coat (MC1) ARTERIAL-04	15	11-Oct-26	27-Oct-26	25-May-26 A	09-Aug-26 A	0.00	142,576.00	142,576.00	0%	100%	67
MKH2-02-003-CN-1360	Bituminous base course for ARTERI	20	28-Oct-26	19-Nov-26	31-May-26 A	13-Aug-26 A	0.00	1,284,309.60	1,284,309.60	0%	100%	83
MKH2-02-003-CN-1410	Tack coat at ARTERIAL-04	14	15-Dec-26	30-Dec-26	14-Jan-27	30-Jan-27	0.00	0.00	73,834.00	0%	0%	-26
MKH2-02-003-CN-1460	Bituminous concrete wearing course	20	31-Dec-26	23-Jan-27	31-Jan-27	23-Feb-27	0.00	0.00	664,894.60	0%	0%	-26
FINISHING WORKS		57	24-Jan-27	14-Mar-27	05-Sep-26 A	13-Apr-27	0.00	287,168.53	754,506.43	0%	38.06%	-26
MKH2-02-003-CN-1510	Installation of Precast Concrete curb	8	24-Jan-27	01-Feb-27	05-Sep-26 A	04-Mar-27	0.00	146,705.38	266,737.05	0%	55%	-26
MKH2-02-003-CN-1550	60mm thick - Interlocking block pave	12	02-Feb-27	15-Feb-27	19-Sep-26 A	22-Mar-27	0.00	140,463.16	401,323.30	0%	35%	-26
MKH2-02-003-CN-1590	Pavement markings [Road-2 -ARTE	9	16-Feb-27	27-Feb-27	23-Mar-27	01-Apr-27	0.00	0.00	76,195.08	0%	0%	-26
MKH2-02-003-CN-1640	Installation of Traffic Signs [Road-2 -	10	28-Feb-27	14-Mar-27	03-Apr-27	13-Apr-27	0.00	0.00	10,251.00	0%	0%	-26
ELECTRICAL WORKS (MKH2-01-007-DAR-TS8-0-SL-DWG-1010		221	21-Sep-26	06-May-27	03-Jun-26 A	24-May-27	8,958.86	579,787.18	647,903.40	1.38%	89.49%	-12
LV NETWORKS		147	21-Sep-26	07-Feb-27	03-Jun-26 A	24-Feb-27	8,958.86	96,748.00	120,868.00	7.41%	80.04%	-14
MKH2-02-003-CN-1900	Installation of Road Crossing Ducts	21	21-Sep-26	15-Oct-26	03-Jun-26 A	04-Jun-26 A	8,958.86	14,472.00	14,472.00	61.9%	100%	113
MKH2-02-003-CN-1910	Installation of Road Crossing Ducts	21	17-Oct-26	09-Nov-26	05-Aug-26 A	07-Aug-26 A	0.00	14,472.00	14,472.00	0%	100%	80
MKH2-02-003-CN-1930	Installation of Road Crossing Ducts	21	10-Nov-26	03-Dec-26	03-Jun-26 A	08-Aug-26 A	0.00	4,824.00	4,824.00	0%	100%	100

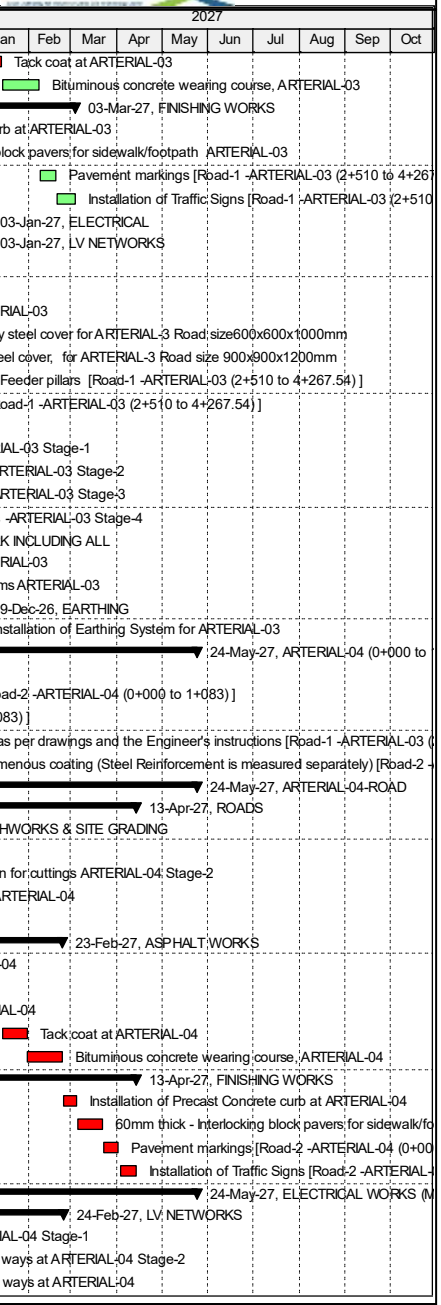

Actual Work | Critical Remaining Work | Remaining Work | Milestone

Date	Revision	Checked	Approved

Activity ID	Activity Name	Original Duration	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Schedule % Complete	Performance % Complete	Variance - BL Project Finish Date
MKH2-02-003-CN-1960	Drawpit with medium duty steel cov	11	05-Dec-26	16-Dec-26	16-Sep-26 A	13-Jan-27	0.00	4,020.00	20,100.00	0%	20%	-24
MKH2-02-003-CN-1980	Drawpit with medium duty steel cov	11	17-Dec-26	29-Dec-26	16-Sep-26 A	24-Sep-26 A	0.00	40,200.00	40,200.00	0%	100%	82
MKH2-02-003-CN-1990	Street Lighting panels [Road-2 -ART	18	02-Jan-27	21-Jan-27	26-Sep-26 A	27-Sep-26 A	0.00	18,760.00	18,760.00	0%	100%	100
MKH2-02-003-CN-2020	Supply and installation of KWH met	14	23-Jan-27	07-Feb-27	08-Feb-27	24-Feb-27	0.00	0.00	8,040.00	0%	0%	-14
LV CABLES		27	08-Feb-27	09-Mar-27	20-Aug-26 A	15-Mar-27	0.00	205,538.58	216,356.40	0%	95%	-2
MKH2-02-003-CN-1730	Installation of Low Voltage Cables -	12	08-Feb-27	21-Feb-27	20-Aug-26 A	24-Aug-26 A	0.00	108,178.20	108,178.20	0%	100%	154
MKH2-02-003-CN-1740	Installation of Low Voltage Cables -	13	23-Feb-27	09-Mar-27	24-Aug-26 A	15-Mar-27	0.00	97,360.38	108,178.20	0%	90%	-2
STREET LIGHTING NETWORK INCLUDING ALL		29	14-Mar-27	13-Apr-27	18-Aug-26 A	27-Apr-27	0.00	276,897.60	307,664.00	0%	90%	-12
MKH2-02-003-CN-1780	Installation of Lighting Poles 2-Arms	15	14-Mar-27	30-Mar-27	18-Aug-26 A	01-Apr-27	0.00	197,784.00	219,760.00	0%	90%	-2
MKH2-02-003-CN-1820	Installation of Lighting Luminaires fc	12	31-Mar-27	13-Apr-27	22-Aug-26 A	27-Apr-27	0.00	79,113.60	87,904.00	0%	90%	-12
EARTHING		20	14-Apr-27	06-May-27	30-Sep-26 A	24-May-27	0.00	603.00	3,015.00	0%	20%	-12
MKH2-02-003-CN-1860	Installation of Earthing System for A	20	14-Apr-27	06-May-27	30-Sep-26 A	24-May-27	0.00	603.00	3,015.00	0%	20%	-12
CONNECTION TO 5th RING ROAD (IF-0+000 to 1+258)		234	15-Jul-26	07-Jun-27	22-Sep-26 A	07-Jul-27	1,543,948.51	739,506.66	3,573,515.75	43.21%	20.69%	-26
EARTHWORKS & SITE GRADING		76	15-Jul-26	21-Oct-26	22-Sep-26 A	15-Dec-26	1,543,948.51	739,506.66	1,604,369.67	96.23%	46.09%	-47
MKH2-02-003-CN-1130	Roadway Excavation for cuttings Cc	21	15-Jul-26	08-Aug-26	22-Sep-26 A	03-Oct-26 A	529,391.12	529,391.12	529,391.12	100%	100%	-47
MKH2-02-003-CN-1140	Roadway Excavation for cuttings Cc	21	09-Aug-26	01-Sep-26	04-Oct-26 A	31-Oct-26	529,391.12	105,878.22	529,391.12	100%	20%	-50
MKH2-02-003-CN-1190	Embankments -to Road connecting	21	02-Sep-26	27-Sep-26	23-Sep-26 A	21-Nov-26	447,984.02	89,596.80	447,984.02	100%	20%	-47
MKH2-02-003-CN-1240	Subgrade for Connecting Road to F	21	28-Sep-26	21-Oct-26	30-Sep-26 A	15-Dec-26	37,182.25	14,640.51	97,603.42	38.1%	15%	-47
ASPHALT WORKS		121	22-Oct-26	10-Apr-27	16-Dec-26	10-May-27	0.00	0.00	1,405,325.00	0%	0%	-26
MKH2-02-003-CN-1290	Aggregate base course at to Road	18	22-Oct-26	11-Nov-26	16-Dec-26	05-Jan-27	0.00	0.00	147,869.00	0%	0%	-47
MKH2-02-003-CN-1340	Prime Coat (MC1) to Road connect	12	12-Nov-26	25-Nov-26	06-Jan-27	19-Jan-27	0.00	0.00	82,919.20	0%	0%	-47
MKH2-02-003-CN-1390	Bituminous base course to Road cc	16	26-Nov-26	14-Dec-26	20-Jan-27	07-Feb-27	0.00	0.00	745,522.40	0%	0%	-47
MKH2-02-003-CN-1440	Tack coat at to Road connecting roa	21	16-Feb-27	16-Mar-27	23-Mar-27	15-Apr-27	0.00	0.00	42,746.00	0%	0%	-26
MKH2-02-003-CN-1490	Bituminous concrete wearing cours	21	17-Mar-27	10-Apr-27	17-Apr-27	10-May-27	0.00	0.00	386,268.40	0%	0%	-26
FINISHING WORKS		47	11-Apr-27	07-Jun-27	11-May-27	07-Jul-27	0.00	0.00	563,821.08	0%	0%	-26
MKH2-02-003-CN-1620	Pavement markings [Road-5 -CONT	16	11-Apr-27	28-Apr-27	11-May-27	01-Jun-27	0.00	0.00	44,236.08	0%	0%	-26
MKH2-02-003-CN-1670	Installation of Traffic Signs [Road-5 -	16	29-Apr-27	20-May-27	02-Jun-27	20-Jun-27	0.00	0.00	17,085.00	0%	0%	-26
MKH2-02-003-CN-1680	Installation of Traffic Signs [Road-5 -	15	22-May-27	07-Jun-27	21-Jun-27	07-Jul-27	0.00	0.00	502,500.00	0%	0%	-26
RAMP-2-IN (0+000 to 0+400)		249	09-Aug-26	04-May-27	05-Aug-26 A	01-Jul-27	129,642.89	152,118.77	752,969.25	17.22%	20.2%	-47
ROADS		172	09-Aug-26	14-Feb-27	05-Aug-26 A	30-Mar-27	129,642.89	152,118.77	508,589.34	25.49%	29.91%	-34
EARTHWORKS & SITE GRADING		56	09-Aug-26	13-Oct-26	05-Aug-26 A	22-Nov-26	129,642.89	120,419.06	131,938.12	98.26%	91.27%	-34
MKH2-02-003-CN-1110	Roadway Excavation for cuttings R/	21	09-Aug-26	01-Sep-26	05-Aug-26 A	27-Oct-26	87,066.10	85,324.78	87,066.10	100%	98%	-47
MKH2-02-003-CN-1170	Embankments -RAMP-02-IN	14	02-Sep-26	17-Sep-26	08-Aug-26 A	09-Nov-26	36,838.72	29,470.97	36,838.72	100%	80%	-44
MKH2-02-003-CN-1220	Subgrade for RAMP-2 IN	21	19-Sep-26	13-Oct-26	13-Aug-26 A	22-Nov-26	5,738.07	5,623.31	8,033.30	71.43%	70%	-34
ASPHALT WORKS		110	14-Oct-26	23-Jan-27	15-Aug-26 A	23-Mar-27	0.00	31,699.71	115,809.50	0%	27.37%	-47
MKH2-02-003-CN-1270	Aggregate base course at RAMP-IN	20	14-Oct-26	05-Nov-26	15-Aug-26 A	15-Dec-26	0.00	8,512.35	12,160.50	0%	70%	-34
MKH2-02-003-CN-1320	Prime Coat (MC1) RAMP-02- IN	14	07-Nov-26	22-Nov-26	31-Aug-26 A	31-Dec-26	0.00	4,727.52	6,753.60	0%	70%	-34
MKH2-02-003-CN-1370	Bituminous base course for RAMP-(	15	23-Nov-26	09-Dec-26	27-Sep-26 A	18-Jan-27	0.00	18,459.84	61,532.80	0%	30%	-34
MKH2-02-003-CN-1420	Tack coat at RAMP-2-IN	14	15-Dec-26	30-Dec-26	08-Feb-27	24-Feb-27	0.00	0.00	3,497.40	0%	0%	-47
MKH2-02-003-CN-1470	Bituminous concrete wearing cours	20	31-Dec-26	23-Jan-27	25-Feb-27	23-Mar-27	0.00	0.00	31,865.20	0%	0%	-47
FINISHING WORKS		57	10-Dec-26	14-Feb-27	19-Jan-27	30-Mar-27	0.00	0.00	260,841.72	0%	0%	-34
MKH2-02-003-CN-1520	Installation of Precast Concrete curt	14	10-Dec-26	26-Dec-26	19-Jan-27	03-Feb-27	0.00	0.00	98,791.50	0%	0%	-34
MKH2-02-003-CN-1560	60mm thick - Interlocking block pave	14	27-Dec-26	11-Jan-27	04-Feb-27	20-Feb-27	0.00	0.00	148,157.10	0%	0%	-34
MKH2-02-003-CN-1600	Pavement markings [Road-3 -RAMI	14	12-Jan-27	27-Jan-27	21-Feb-27	09-Mar-27	0.00	0.00	3,642.12	0%	0%	-34
MKH2-02-003-CN-1650	Installation of Traffic Signs [Road-3 -	15	28-Jan-27	14-Feb-27	14-Mar-27	30-Mar-27	0.00	0.00	10,251.00	0%	0%	-34
ELECTRICAL WORKS (MKH2-01-007-DAR-TS8-0-SL-DWG-1010-(		83	24-Jan-27	04-May-27	24-Mar-27	01-Jul-27	0.00	0.00	244,379.92	0%	0%	-47
LV CABLES		21	24-Jan-27	16-Feb-27	24-Mar-27	17-Apr-27	0.00	0.00	80,162.92	0%	0%	-47
MKH2-02-003-CN-1750	Installation of Low Voltage Cables -	21	24-Jan-27	16-Feb-27	24-Mar-27	17-Apr-27	0.00	0.00	80,162.92	0%	0%	-47
STREET LIGHTING NETWORK INCLUDING ALL		41	17-Feb-27	10-Apr-27	18-Apr-27	07-Jun-27	0.00	0.00	163,212.00	0%	0%	-47
MKH2-02-003-CN-1790	Installation of Lighting Poles 1-Arms	21	17-Feb-27	17-Mar-27	18-Apr-27	11-May-27	0.00	0.00	124,352.00	0%	0%	-47
MKH2-02-003-CN-1830	Installation of Lighting Luminaires fc	20	18-Mar-27	10-Apr-27	12-May-27	07-Jun-27	0.00	0.00	38,860.00	0%	0%	-47
EARTHING		21	11-Apr-27	04-May-27	08-Jun-27	01-Jul-27	0.00	0.00	1,005.00	0%	0%	-47
MKH2-02-003-CN-1870	Installation of Earthing System for F	21	11-Apr-27	04-May-27	08-Jun-27	01-Jul-27	0.00	0.00	1,005.00	0%	0%	-47
RAMP-2-OUT (0+398 to 0+000)		188	02-Sep-26	18-Mar-27	05-Aug-26 A	12-May-27	124,440.37	254,614.00	752,912.29	16.53%	33.82%	-47
ROADS		188	02-Sep-26	18-Mar-27	05-Aug-26 A	12-May-27	124,440.37	181,618.62	508,589.34	24.47%	35.71%	-47

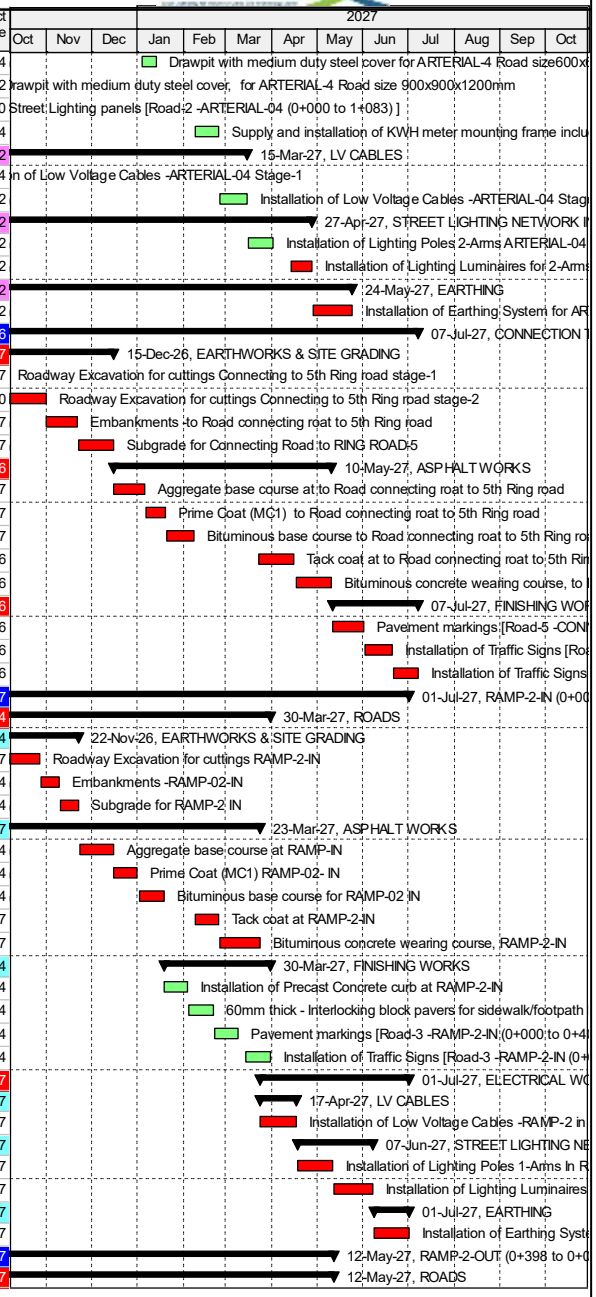

Actual Work | Critical Remaining Work | Remaining Work | Milestone


Date	Revision	Checked	Approved

egis ENJAZCO

MKH2-02-003 - Completion of Infrastructure Works at the Second Industrial City in Makkah UP 31
WBS L5

MODON مدن


Activity ID	Activity Name	Original Duration	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Schedule % Complete	Performance % Complete	Variance - BL Project Finish Date
EARTHWORKS & SITE GRADING		43	02-Sep-26	22-Oct-26	05-Aug-26 A	27-Aug-26 A	124,440.37	131,938.12	131,938.12	94.32%	100%	47
MKH2-02-003-CN-1120	Roadway Excavation for cuttings R/	14	02-Sep-26	17-Sep-26	05-Aug-26 A	17-Aug-26 A	87,066.10	87,066.10	87,066.10	100%	100%	27
MKH2-02-003-CN-1180	Embankments -RAMP-02-out	14	19-Sep-26	05-Oct-26	06-Aug-26 A	22-Aug-26 A	36,838.72	36,838.72	36,838.72	100%	100%	37
MKH2-02-003-CN-1230	Subgrade for RAMP-2 OUT	15	06-Oct-26	22-Oct-26	08-Aug-26 A	27-Aug-26 A	535.55	8,033.30	8,033.30	6.67%	100%	47
ASPHALT WORKS		125	24-Oct-26	08-Feb-27	09-Aug-26 A	08-Apr-27	0.00	49,680.50	115,809.50	0%	42.9%	-47
MKH2-02-003-CN-1280	Aggregate base course at RAMP-O	16	24-Oct-26	10-Nov-26	09-Aug-26 A	30-Aug-26 A	0.00	12,160.50	12,160.50	0%	100%	61
MKH2-02-003-CN-1330	Prime Coat (MC1) RAMP-02- OUT	14	11-Nov-26	26-Nov-26	12-Aug-26 A	31-Aug-26 A	0.00	6,753.60	6,753.60	0%	100%	74
MKH2-02-003-CN-1380	Bituminous base course for RAMP-(	15	28-Nov-26	14-Dec-26	13-Aug-26 A	05-Nov-26	0.00	30,766.40	61,532.80	0%	50%	33
MKH2-02-003-CN-1430	Tack coat at RAMP-2-OUT	14	31-Dec-26	16-Jan-27	25-Feb-27	16-Mar-27	0.00	0.00	3,497.40	0%	0%	-47
MKH2-02-003-CN-1480	Bituminous concrete wearing cours	20	17-Jan-27	08-Feb-27	17-Mar-27	08-Apr-27	0.00	0.00	31,865.20	0%	0%	-47
FINISHING WORKS		49	17-Jan-27	18-Mar-27	17-Mar-27	12-May-27	0.00	0.00	260,841.72	0%	0%	-47
MKH2-02-003-CN-1530	Installation of Precast Concrete curt	12	17-Jan-27	30-Jan-27	17-Mar-27	30-Mar-27	0.00	0.00	98,791.50	0%	0%	-47
MKH2-02-003-CN-1570	60mm thick - Interlocking block pave	14	31-Jan-27	15-Feb-27	31-Mar-27	15-Apr-27	0.00	0.00	148,157.10	0%	0%	-47
MKH2-02-003-CN-1610	Pavement markings [Road-4 -RAMI	11	16-Feb-27	01-Mar-27	17-Apr-27	28-Apr-27	0.00	0.00	3,642.12	0%	0%	-47
MKH2-02-003-CN-1660	Installation of Traffic Signs [Road-4 -	12	02-Mar-27	18-Mar-27	29-Apr-27	12-May-27	0.00	0.00	10,251.00	0%	0%	-47
ELECTRICAL WORKS (MKH2-01-007-DAR-TS8-0-SL-DWG-1010-(		140	15-Dec-26	18-Mar-27	10-Sep-26 A	27-Apr-27	0.00	72,995.39	244,322.95	0%	29.88%	-34
LV CABLES		21	15-Dec-26	07-Jan-27	10-Sep-26 A	30-Nov-26	0.00	24,031.79	80,105.95	0%	30%	33
MKH2-02-003-CN-1760	Installation of Low Voltage Cables -	21	15-Dec-26	07-Jan-27	10-Sep-26 A	30-Nov-26	0.00	24,031.79	80,105.95	0%	30%	33
STREET LIGHTING NETWORK INCLUDING ALL		111	09-Jan-27	01-Mar-27	10-Sep-26 A	13-Apr-27	0.00	48,963.60	163,212.00	0%	30%	-34
MKH2-02-003-CN-1800	Installation of Lighting Poles 1-Arms	19	09-Jan-27	30-Jan-27	10-Sep-26 A	22-Dec-26	0.00	37,305.60	124,352.00	0%	30%	33
MKH2-02-003-CN-1840	Installation of Lighting Luminaires fc	12	15-Feb-27	01-Mar-27	12-Sep-26 A	13-Apr-27	0.00	11,658.00	38,860.00	0%	30%	-34
EARTHING		12	02-Mar-27	18-Mar-27	14-Apr-27	27-Apr-27	0.00	0.00	1,005.00	0%	0%	-34
MKH2-02-003-CN-1880	Installation of Earthing System for F	12	02-Mar-27	18-Mar-27	14-Apr-27	27-Apr-27	0.00	0.00	1,005.00	0%	0%	-34
DEMOLISHING WORKS		116	15-Jun-26	10-Aug-26	08-Apr-26 A	22-Oct-26	189,275.00	155,775.00	189,275.00	100%	82.3%	-62
DEMOLISHING Works		116	15-Jun-26	10-Aug-26	08-Apr-26 A	22-Oct-26	189,275.00	155,775.00	189,275.00	100%	82.3%	-62
MKH2-02-003-CN-1000	Removal of existing curbstone	7	15-Jun-26	22-Jun-26	11-Apr-26 A	06-May-26 A	5,025.00	5,025.00	5,025.00	100%	100%	37
MKH2-02-003-CN-1010	Milling of the existing asphalt layer	14	23-Jun-26	08-Jul-26	07-Oct-26	22-Oct-26	33,500.00	0.00	33,500.00	100%	0%	-90
MKH2-02-003-CN-1020	Removal of the existing asphalt lay(	8	09-Jul-26	18-Jul-26	08-Apr-26 A	16-May-26 A	35,175.00	35,175.00	35,175.00	100%	100%	52
MKH2-02-003-CN-1030	Removal of the existing signages	8	19-Jul-26	27-Jul-26	11-Apr-26 A	06-May-26 A	6,700.00	6,700.00	6,700.00	100%	100%	67
MKH2-02-003-CN-1040	Removal of the existing Street Ligh	12	28-Jul-26	10-Aug-26	11-Apr-26 A	06-May-26 A	108,875.00	108,875.00	108,875.00	100%	100%	79
Open Drain Channels		366	22-Jun-26	14-Jun-27	14-Mar-26 A	26-Jul-27	2,091,676.82	9,330,592.37	10,291,200.00	20.32%	90.67%	-36
Near RAMP-Out Location, from Ch1+640 to Ch 1+899		59	22-Jun-26	02-Sep-26	14-Mar-26 A	28-Jun-26 A	1,470,172.09	1,470,172.09	1,470,172.09	100%	100%	57
MKH2-02-003-CN-2100	Excavation for Channel	21	22-Jun-26	15-Jul-26	14-Mar-26 A	02-Apr-26 A	425,928.72	425,928.72	425,928.72	100%	100%	86
MKH2-02-003-CN-2180	Embankment for Channel Berms	21	16-Jul-26	09-Aug-26	20-Apr-26 A	03-Jun-26 A	53,600.00	53,600.00	53,600.00	100%	100%	57
MKH2-02-003-CN-2250	Riprap Grouting	21	10-Aug-26	02-Sep-26	11-Jun-26 A	28-Jun-26 A	990,643.37	990,643.37	990,643.37	100%	100%	57
Near Ramp- In location from Ch 1+270 to Ch 1+530		155	10-Aug-26	14-Dec-26	02-Apr-26 A	09-Jul-26 A	479,528.55	1,470,171.32	1,470,171.32	32.62%	100%	134
MKH2-02-003-CN-2110	Excavation for Channel	21	10-Aug-26	02-Sep-26	02-Apr-26 A	14-May-26 A	425,928.55	425,928.55	425,928.55	100%	100%	92
MKH2-02-003-CN-2190	Embankment for Channel Berms	21	03-Sep-26	28-Sep-26	04-Jun-26 A	28-Jun-26 A	53,600.00	53,600.00	53,600.00	100%	100%	78
MKH2-02-003-CN-2260	Riprap Grouting	21	21-Nov-26	14-Dec-26	29-Jun-26 A	09-Jul-26 A	0.00	990,642.77	990,642.77	0%	100%	134
Near Ramp- In location from Ch 1+010 to Ch 1+270		44	29-Sep-26	10-Dec-26	16-May-26 A	23-Jul-26 A	141,976.18	1,470,171.32	1,470,171.32	9.66%	100%	119
MKH2-02-003-CN-2130	Excavation for Channel	21	29-Sep-26	22-Oct-26	16-May-26 A	17-Jun-26 A	141,976.18	425,928.55	425,928.55	33.33%	100%	108
MKH2-02-003-CN-2200	Embankment for Channel Berms	21	24-Oct-26	16-Nov-26	28-Jun-26 A	04-Jul-26 A	0.00	53,600.00	53,600.00	0%	100%	115
MKH2-02-003-CN-2270	Riprap Grouting	21	17-Nov-26	10-Dec-26	11-Jul-26 A	23-Jul-26 A	0.00	990,642.77	990,642.77	0%	100%	119
Near Ramp- In location from Ch 0+750 to Ch 1+010		45	17-Nov-26	28-Jan-27	17-Jun-26 A	30-Jul-26 A	0.00	1,470,171.32	1,470,171.32	0%	100%	155
MKH2-02-003-CN-2140	Excavation for Channel	21	17-Nov-26	10-Dec-26	17-Jun-26 A	21-Jul-26 A	0.00	425,928.55	425,928.55	0%	100%	121
MKH2-02-003-CN-2210	Embankment for Channel Berms	21	12-Dec-26	04-Jan-27	05-Jul-26 A	29-Jul-26 A	0.00	53,600.00	53,600.00	0%	100%	135
MKH2-02-003-CN-2280	Riprap Grouting	21	05-Jan-27	28-Jan-27	25-Jul-26 A	30-Jul-26 A	0.00	990,642.77	990,642.77	0%	100%	155
Near Ramp- In location from Ch 0+490 to Ch 0+750		93	05-Jan-27	23-Mar-27	21-Jul-26 A	10-Aug-26 A	0.00	1,470,171.32	1,470,171.32	0%	100%	188
MKH2-02-003-CN-2150	Excavation for Channel	21	05-Jan-27	28-Jan-27	21-Jul-26 A	22-Jul-26 A	0.00	425,928.55	425,928.55	0%	100%	162
MKH2-02-003-CN-2220	Embankment for Channel Berms	21	30-Jan-27	23-Feb-27	30-Jul-26 A	06-Aug-26 A	0.00	53,600.00	53,600.00	0%	100%	170
MKH2-02-003-CN-2290	Riprap Grouting	21	24-Feb-27	23-Mar-27	01-Aug-26 A	10-Aug-26 A	0.00	990,642.77	990,642.77	0%	100%	188
Near Ramp- In location from Ch 0+230 to Ch 0+490		101	24-Feb-27	11-May-27	22-Jul-26 A	03-Sep-26 A	0.00	1,470,171.32	1,470,171.32	0%	100%	209
MKH2-02-003-CN-2160	Excavation for Channel	21	24-Feb-27	23-Mar-27	22-Jul-26 A	23-Jul-26 A	0.00	425,928.55	425,928.55	0%	100%	203
MKH2-02-003-CN-2230	Embankment for Channel Berms	21	24-Mar-27	17-Apr-27	12-Aug-26 A	13-Aug-26 A	0.00	53,600.00	53,600.00	0%	100%	206
MKH2-02-003-CN-2300	Riprap Grouting	21	18-Apr-27	11-May-27	12-Aug-26 A	03-Sep-26 A	0.00	990,642.77	990,642.77	0%	100%	209

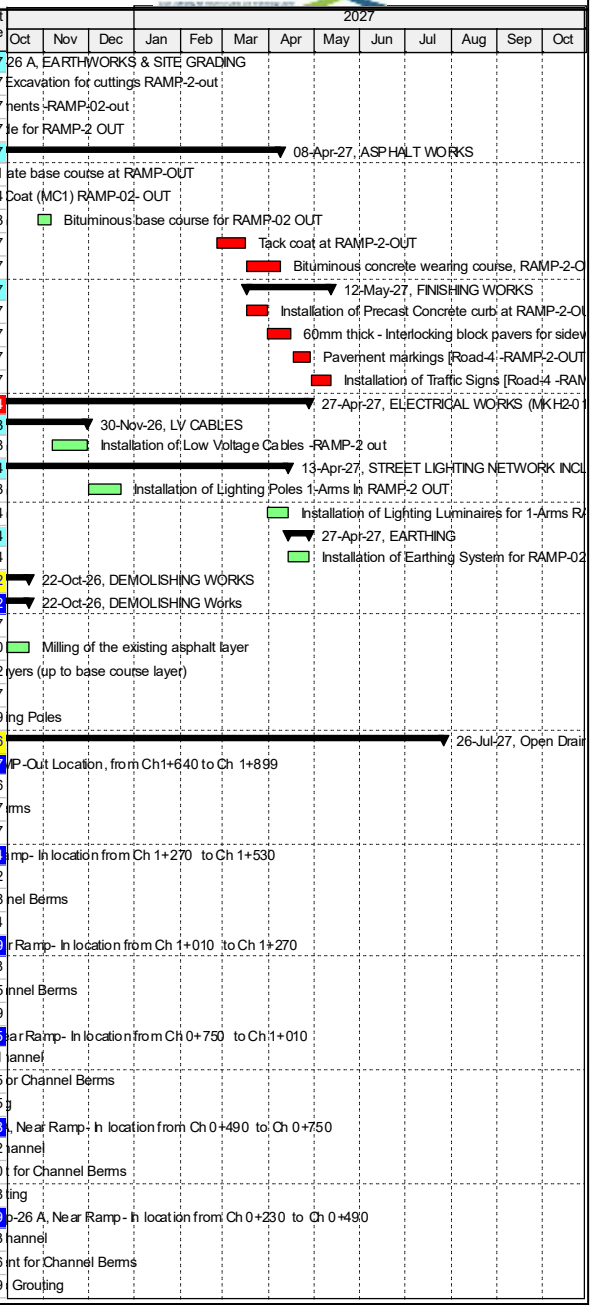

Actual Work
Remaining Work
Critical Remaining Work
Milestone

Date	Revision	Checked	Approved

Activity ID	Activity Name	Original Duration	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Schedule % Complete	Performance % Complete	Variance - BL Project Finish Date
Near Ramp- in location from Ch 0+000 to Ch 0+230		177	30-Mar-27	14-Jun-27	23-Jul-26 A	26-Jul-27	0.00	509,563.69	1,470,171.32	0%	34.66%	-36
MKH2-02-003-CN-2170	Excavation for Channel	21	30-Mar-27	22-Apr-27	23-Jul-26 A	10-Jan-27	0.00	417,409.98	425,928.55	0%	98%	84
MKH2-02-003-CN-2240	Embankment for Channel Berms	21	24-Apr-27	20-May-27	09-Sep-26 A	03-Feb-27	0.00	52,528.00	53,600.00	0%	98%	84
MKH2-02-003-CN-2310	Riprap Grouting	21	22-May-27	14-Jun-27	09-Sep-26 A	26-Jul-27	0.00	39,625.71	990,642.77	0%	4%	-36
TESTING & COMMISSIONING		71	20-Mar-27	26-Jun-27	13-May-27	07-Aug-27	0.00	0.00	5,202,551.60	0%	0%	-36
MKH2-02-003-TC-1000	Test for Electrical Networks	6	08-May-27	13-May-27	03-Jul-27	08-Jul-27	0.00	0.00	1,300,637.90	0%	0%	-45
MKH2-02-003-TC-1010	Test for Box Culvert	6	20-Mar-27	25-Mar-27	13-May-27	23-May-27	0.00	0.00	1,300,637.90	0%	0%	-47
MKH2-02-003-TC-1020	Test for Open Drain channel	10	15-Jun-27	26-Jun-27	27-Jul-27	07-Aug-27	0.00	0.00	1,300,637.90	0%	0%	-36
MKH2-02-003-TC-1030	Test for Roads	6	08-Jun-27	14-Jun-27	08-Jul-27	14-Jul-27	0.00	0.00	1,300,637.90	0%	0%	-26
PROJECT CLOSEOUT & DEMOBILIZATION		107	27-Mar-27	14-Aug-27	24-May-27	26-Sep-27	0.00	0.00	0.00	0%	0%	-36
As-Built DWGs		85	27-Mar-27	19-Jul-27	24-May-27	30-Aug-27	0.00	0.00	0.00	0%	0%	-36
As-Built DWGs Submittals		75	27-Mar-27	07-Jul-27	24-May-27	18-Aug-27	0.00	0.00	0.00	0%	0%	-36
MKH2-02-003-CO-1040	As-Built DWGs Submittal for Electric	7	18-May-27	25-May-27	10-Jul-27	17-Jul-27	0.00	0.00	0.00	0%	0%	-45
MKH2-02-003-CO-1050	As-Built DWGs Submittal for Box C	7	27-Mar-27	03-Apr-27	24-May-27	31-May-27	0.00	0.00	0.00	0%	0%	-47
MKH2-02-003-CO-1060	As-Built DWGs Submittal for Open	10	27-Jun-27	07-Jul-27	08-Aug-27	18-Aug-27	0.00	0.00	0.00	0%	0%	-36
MKH2-02-003-CO-1070	As-Built DWGs Submittal for Roads	7	15-Jun-27	22-Jun-27	27-Jul-27	03-Aug-27	0.00	0.00	0.00	0%	0%	-36
As-Built DWGs Approvals		78	04-Apr-27	19-Jul-27	01-Jun-27	30-Aug-27	0.00	0.00	0.00	0%	0%	-36
MKH2-02-003-CO-1080	As-Built DWGs Approval for Electric	9	26-May-27	05-Jun-27	18-Jul-27	27-Jul-27	0.00	0.00	0.00	0%	0%	-45
MKH2-02-003-CO-1090	As-Built DWGs Approval for Box Cu	7	04-Apr-27	11-Apr-27	01-Jun-27	08-Jun-27	0.00	0.00	0.00	0%	0%	-47
MKH2-02-003-CO-1100	As-Built DWGs Approval for Open D	10	08-Jul-27	19-Jul-27	19-Aug-27	30-Aug-27	0.00	0.00	0.00	0%	0%	-36
MKH2-02-003-CO-1110	As-Built DWGs Approval for Roads	7	23-Jun-27	30-Jun-27	04-Aug-27	11-Aug-27	0.00	0.00	0.00	0%	0%	-36
Demobilization		22	20-Jul-27	14-Aug-27	31-Aug-27	26-Sep-27	0.00	0.00	0.00	0%	0%	-36
MKH2-02-003-CO-1000	Demobilization of Manpower	5	20-Jul-27	25-Jul-27	31-Aug-27	05-Sep-27	0.00	0.00	0.00	0%	0%	-36
MKH2-02-003-CO-1010	Removal of Equipment from Site	5	26-Jul-27	31-Jul-27	06-Sep-27	11-Sep-27	0.00	0.00	0.00	0%	0%	-36
MKH2-02-003-CO-1020	Site Clean Up	5	01-Aug-27	05-Aug-27	12-Sep-27	16-Sep-27	0.00	0.00	0.00	0%	0%	-36
MKH2-02-003-CO-1030	Restoration of Ground Surfaces	7	07-Aug-27	14-Aug-27	18-Sep-27	26-Sep-27	0.00	0.00	0.00	0%	0%	-36

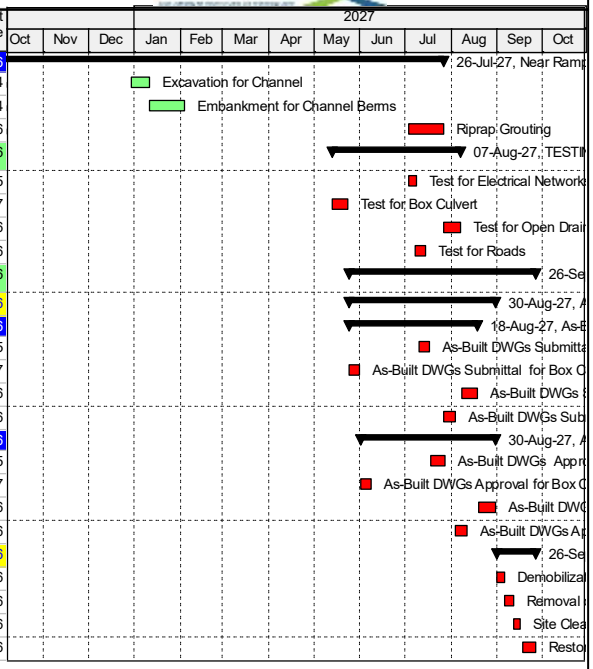

Actual Work
Remaining Work
Critical Remaining Work
Milestone

Date	Revision	Checked	Approved
