
PLAYGROUNDS INITIATIVE - QASSIM, HAIL & TABUK - 25-Oct-2026

Activity ID	Activity Name	O.D	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Schedule % Complete	Performance % Complete	Variance - BL Project Duration
PLAYGROUNDS INITIATIVE - QASSIM, HAIL & TABUK - 25-Oct-2026		301	17-Feb-26 08:00	16-Dec-26 17:00	17-Feb-26 08:00 A	14-Feb-27 15:24	29,430,559.83	24,884,521.11	35,709,993.00	82.42%	69.69%	-51
MILESTONES		301	17-Feb-26 08:00	16-Dec-26 17:00	17-Feb-26 08:00 A	14-Feb-27 15:24	0.00	0.00	0.00	0%	0%	-51
GENERAL MILESTONES		301	17-Feb-26 08:00	16-Dec-26 17:00	17-Feb-26 08:00 A	14-Feb-27 15:24	0.00	0.00	0.00	0%	0%	-51
PG-GN-MS-10	Project Commencement Date	0	17-Feb-26 08:00		17-Feb-26 08:00 A		0.00	0.00	0.00	100%	100%	0
PG-GN-MS-20	Project Completion Date	0		16-Dec-26 17:00		14-Feb-27 15:24	0.00	0.00	0.00	0%	0%	0
PG-GN-MS-30	Project Durations(Completed)	101	17-Feb-26 08:00	24-Jun-26 17:00	17-Feb-26 08:00 A	24-Jun-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-GN-MS-30_R	Project Durations(Remaining)	148	25-Jun-26 08:00	15-Dec-26 17:00	01-Jul-26 08:00 A	15-Dec-26 14:48	0.00	0.00	0.00	68.92%	69%	5
CONTRACUAL MILESTONES		239	05-May-26 17:00	16-Dec-26 17:00	05-May-26 17:00 A	14-Feb-27 15:24	0.00	0.00	0.00	0%	0%	-51
PG-IN-MS-10	Site Preparation, Work Plans, Schedule ,Drawings Submittals	0		04-Aug-26 17:00		16-Sep-26 12:00 A	0.00	0.00	0.00	100%	100%	0
PG-IN-MS-20	Completion of Earthworks (Cut and fill) For Site Layout	0		05-May-26 17:00		05-May-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-IN-MS-30	Completion of Toilet Building	0		28-Oct-26 17:00		05-Nov-26 16:36	0.00	0.00	0.00	0%	0%	0
PG-IN-MS-40	Completion of Landscape Works	0		16-Dec-26 17:00		10-Jan-27 16:12	0.00	0.00	0.00	0%	0%	0
PG-IN-MS-50	Completion of Playground Works	0		07-Dec-26 17:00		14-Dec-26 10:48	0.00	0.00	0.00	0%	0%	0
PG-IN-MS-60	Substantial Completion - All Works	0		16-Dec-26 17:00		14-Feb-27 15:24	0.00	0.00	0.00	0%	0%	0
QASSIM		301	17-Feb-26 08:00	16-Dec-26 17:00	17-Feb-26 08:00 A	14-Feb-27 15:24	14,543,486.11	12,407,011.96	17,537,540.00	82.93%	70.75%	-51
MOBILIZATION		29	17-Feb-26 08:00	29-Mar-26 10:00	17-Feb-26 08:00 A	28-Mar-26 17:00 A	0.00	0.00	0.00	0%	0%	0
TEMPORARY CAMP		28	17-Feb-26 08:00	28-Mar-26 09:00	17-Feb-26 08:00 A	27-Mar-26 17:00 A	0.00	0.00	0.00	0%	0%	0
PG-Q-MOB-CAM-10	Temporary Underground Utilities works	28	17-Feb-26 08:00	28-Mar-26 09:00	17-Feb-26 08:00 A	27-Mar-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-Q-MOB-CAM-20	Temporary Porta-Cabins	21	26-Feb-26 08:00	28-Mar-26 09:00	26-Feb-26 08:00 A	27-Mar-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-Q-MOB-CAM-30	Temporary Toilets	21	26-Feb-26 08:00	28-Mar-26 09:00	26-Feb-26 08:00 A	27-Mar-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-Q-MOB-CAM-40	Temporary Mosque	13	08-Mar-26 08:00	28-Mar-26 09:00	08-Mar-26 08:00 A	27-Mar-26 17:00 A	0.00	0.00	0.00	100%	100%	0
SITE OFFICES		29	17-Feb-26 08:00	29-Mar-26 10:00	17-Feb-26 08:00 A	28-Mar-26 17:00 A	0.00	0.00	0.00	0%	0%	0
PG-Q-MOB-SO-10	Temporary Underground Utilities works	29	17-Feb-26 08:00	29-Mar-26 10:00	17-Feb-26 08:00 A	28-Mar-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-Q-MOB-SO-20	Temporary Porta-Cabins	22	26-Feb-26 08:00	29-Mar-26 10:00	26-Feb-26 08:00 A	28-Mar-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-Q-MOB-SO-30	Temporary Toilets	22	26-Feb-26 08:00	29-Mar-26 10:00	26-Feb-26 08:00 A	28-Mar-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-Q-MOB-SO-40	Temporary Mosque	16	05-Mar-26 08:00	29-Mar-26 10:00	05-Mar-26 08:00 A	28-Mar-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-Q-MOB-SO-50	Car Parking Area	10	12-Mar-26 08:00	29-Mar-26 10:00	12-Mar-26 08:00 A	28-Mar-26 17:00 A	0.00	0.00	0.00	100%	100%	0
GENERAL REQUIEREMENTS		57	17-Feb-26 08:00	30-Apr-26 10:00	17-Feb-26 08:00 A	29-Apr-26 17:00 A	0.00	0.00	0.00	0%	0%	0
PG-Q-GEN-10	QA/QC Submission Plan	16	12-Mar-26 08:00	04-Apr-26 13:00	12-Mar-26 08:00 A	04-Apr-26 12:00 A	0.00	0.00	0.00	100%	100%	0
PG-Q-GEN-20	HSSE Submission Plan	57	17-Feb-26 08:00	30-Apr-26 10:00	17-Feb-26 08:00 A	29-Apr-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-Q-GEN-30	Surveying report Submission Plan	57	17-Feb-26 08:00	30-Apr-26 10:00	17-Feb-26 08:00 A	29-Apr-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-Q-GEN-40	Baseline Submission	6	28-Feb-26 08:00	07-Mar-26 10:00	28-Feb-26 08:00 A	05-Mar-26 17:00 A	0.00	0.00	0.00	100%	100%	0
ENGINEERING		199	17-Feb-26 08:00	16-Aug-26 17:00	17-Feb-26 08:00 A	25-Oct-26 15:24	526,126.20	526,126.20	526,126.20	100%	100%	-59
SHOP DRAWINGS SUBMITTALS		168	17-Feb-26 08:00	04-Aug-26 17:00	17-Feb-26 08:00 A	25-Oct-26 15:24	0.00	0.00	0.00	0%	0%	-59
STRUCTURAL DRAWINGS		125	17-Feb-26 08:00	06-Jul-26 17:00	17-Feb-26 08:00 A	11-Jul-26 17:00 A	0.00	0.00	0.00	0%	0%	-4
PROJECT FENCE		19	29-Apr-26 08:00	21-May-26 10:00	29-Apr-26 08:00 A	20-May-26 17:00 A	0.00	0.00	0.00	0%	0%	0
PG-Q-EN-ST-SD-SB-10	Excavation Drawings	19	29-Apr-26 08:00	21-May-26 10:00	29-Apr-26 08:00 A	20-May-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-Q-EN-ST-SD-SB-20	Foundation Drawings	19	29-Apr-26 08:00	21-May-26 10:00	29-Apr-26 08:00 A	20-May-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PADEL PLAYGROUND FENCE		19	29-Apr-26 08:00	21-May-26 10:00	29-Apr-26 08:00 A	20-May-26 17:00 A	0.00	0.00	0.00	0%	0%	0
PG-Q-EN-ST-SD-SB-30	Excavation Drawings	19	29-Apr-26 08:00	21-May-26 10:00	29-Apr-26 08:00 A	20-May-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-Q-EN-ST-SD-SB-40	Foundation Drawings	19	29-Apr-26 08:00	21-May-26 10:00	29-Apr-26 08:00 A	20-May-26 17:00 A	0.00	0.00	0.00	100%	100%	0
AIR DOME		10	25-Jun-26 08:00	06-Jul-26 17:00	01-Jul-26 08:00 A	11-Jul-26 17:00 A	0.00	0.00	0.00	0%	0%	1
PG-Q-EN-ST-SD-SB-50	Excavation Drawings	8	25-Jun-26 08:00	04-Jul-26 17:00	01-Jul-26 08:00 A	02-Jul-26 17:00 A	0.00	0.00	0.00	100%	100%	6
PG-Q-EN-ST-SD-SB-60	Foundation Drawings	10	25-Jun-26 08:00	06-Jul-26 17:00	07-Jul-26 08:00 A	11-Jul-26 17:00 A	0.00	0.00	0.00	100%	100%	6
TOILET BUILDING		43	17-Feb-26 08:00	14-Apr-26 10:00	17-Feb-26 08:00 A	13-Apr-26 17:00 A	0.00	0.00	0.00	0%	0%	0
PG-Q-EN-ST-SD-SB-70	Excavation Drawings	43	17-Feb-26 08:00	14-Apr-26 10:00	17-Feb-26 08:00 A	13-Apr-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-Q-EN-ST-SD-SB-80	Foundation Drawings	41	19-Feb-26 08:00	14-Apr-26 10:00	19-Feb-26 08:00 A	13-Apr-26 17:00 A	0.00	0.00	0.00	100%	100%	0
WATER STORAGE TANK		41	19-Feb-26 08:00	14-Apr-26 10:00	19-Feb-26 08:00 A	13-Apr-26 17:00 A	0.00	0.00	0.00	0%	0%	0
PG-Q-EN-ST-SD-SB-100	Foundation Drawings	39	23-Feb-26 08:00	14-Apr-26 10:00	23-Feb-26 08:00 A	13-Apr-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-Q-EN-ST-SD-SB-90	Excavation Drawings	41	19-Feb-26 08:00	14-Apr-26 10:00	19-Feb-26 08:00 A	13-Apr-26 17:00 A	0.00	0.00	0.00	100%	100%	0
SEPTIC TANK		13	28-Apr-26 08:00	13-May-26 10:00	28-Apr-26 08:00 A	12-May-26 17:00 A	0.00	0.00	0.00	0%	0%	0
PG-Q-EN-ST-SD-SB-110	Reinforcement Detail Drawings	13	28-Apr-26 08:00	13-May-26 10:00	28-Apr-26 08:00 A	12-May-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-Q-EN-ST-SD-SB-120	Concrete Detail Drawings	13	28-Apr-26 08:00	13-May-26 10:00	28-Apr-26 08:00 A	12-May-26 17:00 A	0.00	0.00	0.00	100%	100%	0
ARCHITECTURAL DRAWINGS		158	19-Feb-26 08:00	23-Jul-26 17:00	19-Feb-26 08:00 A	10-Sep-26 12:00 A	0.00	0.00	0.00	0%	0%	-42
TOILET BUILDING		42	19-Feb-26 08:00	15-Apr-26 10:36	19-Feb-26 08:00 A	15-Apr-26 09:36 A	0.00	0.00	0.00	0%	0%	0
PG-Q-EN-AR-SD-SB-10	Ground Floor Plan	40	19-Feb-26 08:00	13-Apr-26 10:36	19-Feb-26 08:00 A	13-Apr-26 09:36 A	0.00	0.00	0.00	100%	100%	0
PG-Q-EN-AR-SD-SB-100	Cladding Details	34	01-Mar-26 08:00	14-Apr-26 10:00	01-Mar-26 08:00 A	13-Apr-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-Q-EN-AR-SD-SB-20	Roof Floor Plan	37	25-Feb-26 08:00	14-Apr-26 10:00	25-Feb-26 08:00 A	13-Apr-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-Q-EN-AR-SD-SB-30	Elevations	34	01-Mar-26 08:00	14-Apr-26 08:24	01-Mar-26 08:00 A	13-Apr-26 15:24 A	0.00	0.00	0.00	100%	100%	0
PG-Q-EN-AR-SD-SB-40	Sections	32	03-Mar-26 08:00	13-Apr-26 12:12	03-Mar-26 08:00 A	13-Apr-26 11:12 A	0.00	0.00	0.00	100%	100%	0
PG-Q-EN-AR-SD-SB-50	Floor Finish Layout	36	25-Feb-26 08:00	13-Apr-26 09:48	25-Feb-26 08:00 A	13-Apr-26 08:48 A	0.00	0.00	0.00	100%	100%	0
PG-Q-EN-AR-SD-SB-60	Reflected Ceiling Layout	37	25-Feb-26 08:00	13-Apr-26 12:12	25-Feb-26 08:00 A	13-Apr-26 11:12 A	0.00	0.00	0.00	100%	100%	0
PG-Q-EN-AR-SD-SB-70	Enlarged Toilets Layout	38	25-Feb-26 08:00	15-Apr-26 10:36	25-Feb-26 08:00 A	15-Apr-26 09:36 A	0.00	0.00	0.00	100%	100%	0
PG-Q-EN-AR-SD-SB-80	Doors & Windows Schedule	35	01-Mar-26 08:00	15-Apr-26 09:48	01-Mar-26 08:00 A	15-Apr-26 08:48 A	0.00	0.00	0.00	100%	100%	0
PG-Q-EN-AR-SD-SB-90	Aluminum Work	35	01-Mar-26 08:00	15-Apr-26 09:48	01-Mar-26 08:00 A	15-Apr-26 08:48 A	0.00	0.00	0.00	100%	100%	0
AIR DOME		15	07-Jul-26 08:00	23-Jul-26 17:00	14-Aug-26 08:00 A	10-Sep-26 12:00 A	0.00	0.00	0.00	0%	0%	-9
PG-Q-EN-AR-SD-SB-110	Membrane & Insulation Details	15	07-Jul-26 08:00	23-Jul-26 17:00	14-Aug-26 08:00 A	10-Sep-26 12:00 A	0.00	0.00	0.00	100%	100%	-9
PG-Q-EN-AR-SD-SB-120	Steel Cable System	15	07-Jul-26 08:00	23-Jul-26 17:00	14-Aug-26 08:00 A	10-Sep-26 12:00 A	0.00	0.00	0.00	100%	100%	-9
PG-Q-EN-AR-SD-SB-130	Doors & Access Sytem Drawings	15	07-Jul-26 08:00	23-Jul-26 17:00	14-Aug-26 08:00 A	10-Sep-26 12:00 A	0.00	0.00	0.00	100%	100%	-9
LANDSCAPE DRAWINGS		39	23-Feb-26 08:00	14-Apr-26 10:00	23-Feb-26 08:00 A	13-Apr-26 17:00 A	0.00	0.00	0.00	0%	0%	0
PG-Q-EN-LS-SD-SB-10	Hardscape Layout Plan	36	23-Feb-26 08:00	11-Apr-26 10:00	23-Feb-26 08:00 A	09-Apr-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-Q-EN-LS-SD-SB-100	Padel Playground Layout	39	23-Feb-26 08:00	14-Apr-26 10:00	23-Feb-26 08:00 A	13-Apr-26 17:00 A	0.00	0.00	0.00	100%	100%	0

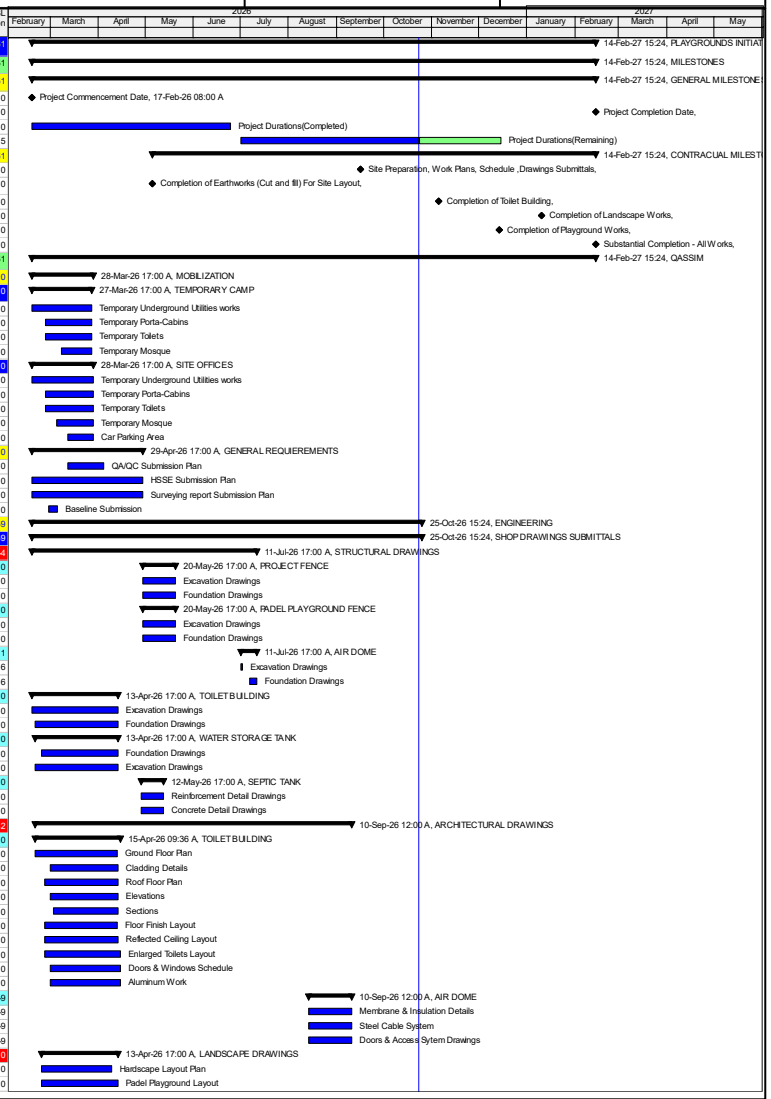

Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining W...
Milestone
summary

Baseline Schedule Rev.00

PLAYGROUNDS INITIATIVE - QASSIM, HAIL & TABUK - 25-Oct-2026

Activity ID	Activity Name	O.D	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Schedule % Complete	Performance % Complete	Variance - BL Project Duration
PG-Q-EN-LS-SD-SB-110	Basketball Playground Layout	39	23-Feb-26 08:00	14-Apr-26 10:00	23-Feb-26 08:00 A	13-Apr-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-Q-EN-LS-SD-SB-120	Playground Details	39	23-Feb-26 08:00	14-Apr-26 10:00	23-Feb-26 08:00 A	13-Apr-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-Q-EN-LS-SD-SB-130	Padel Fence Elevation & Details	39	23-Feb-26 08:00	14-Apr-26 10:00	23-Feb-26 08:00 A	13-Apr-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-Q-EN-LS-SD-SB-20	Interlock Tile Details	36	23-Feb-26 08:00	11-Apr-26 10:00	23-Feb-26 08:00 A	09-Apr-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-Q-EN-LS-SD-SB-30	Stamped Concrete Pattern & Section	36	23-Feb-26 08:00	11-Apr-26 10:00	23-Feb-26 08:00 A	09-Apr-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-Q-EN-LS-SD-SB-40	Tartan Flooring Layout & Details	36	23-Feb-26 08:00	11-Apr-26 10:00	23-Feb-26 08:00 A	09-Apr-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-Q-EN-LS-SD-SB-50	Bike Path Layout & Details	36	23-Feb-26 08:00	11-Apr-26 10:00	23-Feb-26 08:00 A	09-Apr-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-Q-EN-LS-SD-SB-60	Walking Path layout & Details	36	23-Feb-26 08:00	11-Apr-26 10:00	23-Feb-26 08:00 A	09-Apr-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-Q-EN-LS-SD-SB-70	Tree Planting Plan & Details	39	23-Feb-26 08:00	14-Apr-26 10:00	23-Feb-26 08:00 A	13-Apr-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-Q-EN-LS-SD-SB-80	Traffic Sign Location & Details	39	23-Feb-26 08:00	14-Apr-26 10:00	23-Feb-26 08:00 A	13-Apr-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-Q-EN-LS-SD-SB-90	Football Playground Layout	39	23-Feb-26 08:00	14-Apr-26 10:00	23-Feb-26 08:00 A	13-Apr-26 17:00 A	0.00	0.00	0.00	100%	100%	0
MECHANICAL DRAWINGS		143	28-Feb-26 08:00	15-Jul-26 17:00	28-Feb-26 08:00 A	25-Oct-26 15:24	0.00	0.00	0.00	0%	0%	-86
WATER SUPPLY SYSTEM		32	28-Feb-26 08:00	11-Apr-26 10:00	28-Feb-26 08:00 A	09-Apr-26 17:00 A	0.00	0.00	0.00	0%	0%	0
PG-Q-EN-ME-SD-SB-10	Cold & Hot Water Piping Layout	28	04-Mar-26 08:00	11-Apr-26 10:00	04-Mar-26 08:00 A	09-Apr-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-Q-EN-ME-SD-SB-20	Pump Room Layout	32	28-Feb-26 08:00	11-Apr-26 10:00	28-Feb-26 08:00 A	09-Apr-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-Q-EN-ME-SD-SB-30	Booster Pump Details	28	04-Mar-26 08:00	11-Apr-26 10:00	04-Mar-26 08:00 A	09-Apr-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-Q-EN-ME-SD-SB-40	GRP Water Tank Details	24	09-Mar-26 08:00	11-Apr-26 10:00	09-Mar-26 08:00 A	09-Apr-26 17:00 A	0.00	0.00	0.00	100%	100%	0
SEWER AND DRAINAGE SYSTEM		28	04-Mar-26 08:00	11-Apr-26 10:00	04-Mar-26 08:00 A	09-Apr-26 17:00 A	0.00	0.00	0.00	0%	0%	0
PG-Q-EN-ME-SD-SB-50	Drainage Layout	28	04-Mar-26 08:00	11-Apr-26 10:00	04-Mar-26 08:00 A	09-Apr-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-Q-EN-ME-SD-SB-60	Floor Drains & Cleanouts Details	24	09-Mar-26 08:00	11-Apr-26 10:00	09-Mar-26 08:00 A	09-Apr-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-Q-EN-ME-SD-SB-70	Inspection Chamber Details	21	12-Mar-26 08:00	11-Apr-26 10:00	12-Mar-26 08:00 A	09-Apr-26 17:00 A	0.00	0.00	0.00	100%	100%	0
IRRIGATION SYSTEM		24	09-Mar-26 08:00	11-Apr-26 10:00	09-Mar-26 08:00 A	09-Apr-26 17:00 A	0.00	0.00	0.00	0%	0%	0
PG-Q-EN-ME-SD-SB-80	HDPE Pipe Routing	24	09-Mar-26 08:00	11-Apr-26 10:00	09-Mar-26 08:00 A	09-Apr-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-Q-EN-ME-SD-SB-90	Irrigation Network Layout	21	12-Mar-26 08:00	11-Apr-26 10:00	12-Mar-26 08:00 A	09-Apr-26 17:00 A	0.00	0.00	0.00	100%	100%	0
AIR DOME		18	25-Jun-26 08:00	15-Jul-26 17:00	30-Jul-26 08:00 A	25-Oct-26 15:24	0.00	0.00	0.00	0%	0%	-56
PG-Q-EN-ME-SD-SB-100	Air Package and HVAC System Drawings	18	25-Jun-26 08:00	15-Jul-26 17:00	30-Jul-26 08:00 A	25-Oct-26 15:24	0.00	0.00	0.00	100%	90%	-56
ELECTRICAL DRAWINGS		102	11-May-26 08:00	04-Aug-26 17:00	11-May-26 08:00 A	25-Oct-26 14:36	0.00	0.00	0.00	0%	0%	-69
POWER AND LIGHTING SYSTEM		27	11-May-26 08:00	16-Jun-26 10:00	11-May-26 08:00 A	15-Jun-26 17:00 A	0.00	0.00	0.00	0%	0%	0
PG-Q-EN-EL-SD-SB-10	Main Distribution Board (MDB) Layout	27	11-May-26 08:00	16-Jun-26 10:00	11-May-26 08:00 A	15-Jun-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-Q-EN-EL-SD-SB-20	Pump Room Power Panel	27	11-May-26 08:00	16-Jun-26 10:00	11-May-26 08:00 A	15-Jun-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-Q-EN-EL-SD-SB-30	Street Lighting Power Panel	27	11-May-26 08:00	16-Jun-26 10:00	11-May-26 08:00 A	15-Jun-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-Q-EN-EL-SD-SB-40	Site Lighting Pole Layout	27	11-May-26 08:00	16-Jun-26 10:00	11-May-26 08:00 A	15-Jun-26 17:00 A	0.00	0.00	0.00	100%	100%	0
ELV SYSTEM		27	11-May-26 08:00	16-Jun-26 10:00	11-May-26 08:00 A	15-Jun-26 17:00 A	0.00	0.00	0.00	0%	0%	0
PG-Q-EN-EL-SD-SB-50	Telecom & Data Layout	27	11-May-26 08:00	16-Jun-26 10:00	11-May-26 08:00 A	15-Jun-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-Q-EN-EL-SD-SB-60	CCTV Camera Layout	27	11-May-26 08:00	16-Jun-26 10:00	11-May-26 08:00 A	15-Jun-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-Q-EN-EL-SD-SB-70	Access Control Layout	27	11-May-26 08:00	16-Jun-26 10:00	11-May-26 08:00 A	15-Jun-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-Q-EN-EL-SD-SB-80	AV System Layout	27	11-May-26 08:00	16-Jun-26 10:00	11-May-26 08:00 A	15-Jun-26 17:00 A	0.00	0.00	0.00	100%	100%	0
FIRE ALARM SYSTEM		27	11-May-26 08:00	16-Jun-26 10:00	11-May-26 08:00 A	15-Jun-26 17:00 A	0.00	0.00	0.00	0%	0%	0
PG-Q-EN-EL-SD-SB-100	Detector & Manual Call Point Details	27	11-May-26 08:00	16-Jun-26 10:00	11-May-26 08:00 A	15-Jun-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-Q-EN-EL-SD-SB-110	Control Panel Wiring Diagram	27	11-May-26 08:00	16-Jun-26 10:00	11-May-26 08:00 A	15-Jun-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-Q-EN-EL-SD-SB-90	Fire Alarm Layout	27	11-May-26 08:00	16-Jun-26 10:00	11-May-26 08:00 A	15-Jun-26 17:00 A	0.00	0.00	0.00	100%	100%	0
AIR DOME		17	16-Jul-26 08:00	04-Aug-26 17:00	30-Jul-26 08:00 A	25-Oct-26 14:36	0.00	0.00	0.00	0%	0%	-57
PG-Q-EN-EL-SD-SB-120	Power & Lighting System Drawings	10	16-Jul-26 08:00	27-Jul-26 17:00	30-Jul-26 08:00 A	24-Oct-26 17:00	0.00	0.00	0.00	100%	90%	-63
PG-Q-EN-EL-SD-SB-130	Generators Details	15	16-Jul-26 08:00	02-Aug-26 17:00	30-Jul-26 08:00 A	25-Oct-26 12:00	0.00	0.00	0.00	100%	90%	-59
PG-Q-EN-EL-SD-SB-140	Smart Dome System Drawings	17	16-Jul-26 08:00	04-Aug-26 17:00	30-Jul-26 08:00 A	25-Oct-26 14:36	0.00	0.00	0.00	100%	90%	-57
SHOP DRAWINGS APPROVALS		172	19-Feb-26 08:00	16-Aug-26 17:00	19-Feb-26 08:00 A	21-Sep-26 08:48 A	0.00	0.00	0.00	0%	0%	-30
STRUCTURAL DRAWINGS		130	19-Feb-26 08:00	14-Jul-26 17:00	19-Feb-26 08:00 A	12-Jul-26 17:00 A	0.00	0.00	0.00	0%	0%	2
PROJECT FENCE		7	13-May-26 08:00	21-May-26 10:00	13-May-26 08:00 A	20-May-26 17:00 A	0.00	0.00	0.00	0%	0%	0
PG-Q-EN-ST-SD-AP-10	Excavation Drawings	7	13-May-26 08:00	21-May-26 10:00	13-May-26 08:00 A	20-May-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-Q-EN-ST-SD-AP-20	Foundation Drawings	7	13-May-26 08:00	21-May-26 10:00	13-May-26 08:00 A	20-May-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PADEL PLAYGROUND FENCE		9	11-May-26 08:00	21-May-26 10:00	11-May-26 08:00 A	20-May-26 17:00 A	0.00	0.00	0.00	0%	0%	0
PG-Q-EN-ST-SD-AP-30	Excavation Drawings	9	11-May-26 08:00	21-May-26 10:00	11-May-26 08:00 A	20-May-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-Q-EN-ST-SD-AP-40	Foundation Drawings	9	11-May-26 08:00	21-May-26 10:00	11-May-26 08:00 A	20-May-26 17:00 A	0.00	0.00	0.00	100%	100%	0
AIR DOME		9	05-Jul-26 08:00	14-Jul-26 17:00	06-Jul-26 08:00 A	12-Jul-26 17:00 A	0.00	0.00	0.00	0%	0%	3
PG-Q-EN-ST-SD-AP-50	Excavation Drawings	4	05-Jul-26 08:00	08-Jul-26 17:00	06-Jul-26 08:00 A	07-Jul-26 17:00 A	0.00	0.00	0.00	100%	100%	2
PG-Q-EN-ST-SD-AP-60	Foundation Drawings	7	07-Jul-26 08:00	14-Jul-26 17:00	08-Jul-26 08:00 A	12-Jul-26 17:00 A	0.00	0.00	0.00	100%	100%	3
TOILET BUILDING		44	19-Feb-26 08:00	18-Apr-26 10:00	19-Feb-26 08:00 A	16-Apr-26 17:00 A	0.00	0.00	0.00	0%	0%	0
PG-Q-EN-ST-SD-AP-70	Excavation Drawings	44	19-Feb-26 08:00	18-Apr-26 10:00	19-Feb-26 08:00 A	16-Apr-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-Q-EN-ST-SD-AP-80	Foundation Drawings	36	02-Mar-26 08:00	18-Apr-26 10:00	02-Mar-26 08:00 A	16-Apr-26 17:00 A	0.00	0.00	0.00	100%	100%	0
WATER STORAGE TANK		42	23-Feb-26 08:00	18-Apr-26 10:00	23-Feb-26 08:00 A	16-Apr-26 17:00 A	0.00	0.00	0.00	0%	0%	0
PG-Q-EN-ST-SD-AP-100	Foundation Drawings	34	04-Mar-26 08:00	18-Apr-26 10:00	04-Mar-26 08:00 A	16-Apr-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-Q-EN-ST-SD-AP-90	Excavation Drawings	42	23-Feb-26 08:00	18-Apr-26 10:00	23-Feb-26 08:00 A	16-Apr-26 17:00 A	0.00	0.00	0.00	100%	100%	0
SEPTIC TANK		3	11-May-26 08:00	14-May-26 10:00	11-May-26 08:00 A	13-May-26 17:00 A	0.00	0.00	0.00	0%	0%	0
PG-Q-EN-ST-SD-AP-110	Reinforcement Detail Drawings	3	11-May-26 08:00	14-May-26 10:00	11-May-26 08:00 A	13-May-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-Q-EN-ST-SD-AP-120	Concrete Detail Drawings	3	11-May-26 08:00	14-May-26 10:00	11-May-26 08:00 A	13-May-26 17:00 A	0.00	0.00	0.00	100%	100%	0
ARCHITECTURAL DRAWINGS		166	25-Feb-26 08:00	01-Aug-26 17:00	25-Feb-26 08:00 A	21-Sep-26 08:48 A	0.00	0.00	0.00	0%	0%	-43
TOILET BUILDING		40	25-Feb-26 08:00	18-Apr-26 10:00	25-Feb-26 08:00 A	16-Apr-26 17:00 A	0.00	0.00	0.00	0%	0%	0
PG-Q-EN-AR-SD-AP-10	Ground Floor Plan	40	25-Feb-26 08:00	18-Apr-26 10:00	25-Feb-26 08:00 A	16-Apr-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-Q-EN-AR-SD-AP-100	Cladding Details	33	05-Mar-26 08:00	18-Apr-26 10:00	05-Mar-26 08:00 A	16-Apr-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-Q-EN-AR-SD-AP-20	Roof Floor Plan	37	01-Mar-26 08:00	18-Apr-26 10:00	01-Mar-26 08:00 A	16-Apr-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-Q-EN-AR-SD-AP-30	Elevations	34	04-Mar-26 08:00	18-Apr-26 10:00	04-Mar-26 08:00 A	16-Apr-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-Q-EN-AR-SD-AP-40	Sections	31	08-Mar-26 08:00	18-Apr-26 10:00	08-Mar-26 08:00 A	16-Apr-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-Q-EN-AR-SD-AP-50	Floor Finish Layout	35	03-Mar-26 08:00	18-Apr-26 10:00	03-Mar-26 08:00 A	16-Apr-26 17:00 A	0.00	0.00	0.00	100%	100%	0




Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining W...
Milestone
summary

Baseline Schedule Rev.00

PLAYGROUNDS INITIATIVE - QASSIM, HAIL & TABUK - 25-Oct-2026

Activity ID	Activity Name	O.D	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Schedule % Complete	Performance % Complete	Variance - BL Project Duration
PG-Q-EN-AR-SD-AP-60	Reflected Ceiling Layout	35	03-Mar-26 08:00	18-Apr-26 10:00	03-Mar-26 08:00 A	16-Apr-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-Q-EN-AR-SD-AP-70	Enlarged Toilets Layout	35	03-Mar-26 08:00	18-Apr-26 10:00	03-Mar-26 08:00 A	16-Apr-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-Q-EN-AR-SD-AP-80	Doors & Windows Schedule	34	04-Mar-26 08:00	18-Apr-26 10:00	04-Mar-26 08:00 A	16-Apr-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-Q-EN-AR-SD-AP-90	Aluminum Work	33	05-Mar-26 08:00	18-Apr-26 10:00	05-Mar-26 08:00 A	16-Apr-26 17:00 A	0.00	0.00	0.00	100%	100%	0
AIR DOME		7	25-Jul-26 08:00	01-Aug-26 17:00	20-Aug-26 08:00 A	21-Sep-26 08:48 A	0.00	0.00	0.00	0%	0%	-20
PG-Q-EN-AR-SD-AP-110	Membrane & Insulation Details	7	25-Jul-26 08:00	01-Aug-26 17:00	20-Aug-26 08:00 A	21-Sep-26 08:48 A	0.00	0.00	0.00	100%	100%	-20
PG-Q-EN-AR-SD-AP-120	Steel Cable System	7	25-Jul-26 08:00	01-Aug-26 17:00	20-Aug-26 08:00 A	21-Sep-26 08:48 A	0.00	0.00	0.00	100%	100%	-20
PG-Q-EN-AR-SD-AP-130	Doors & Access Sytem Drawings	7	25-Jul-26 08:00	01-Aug-26 17:00	20-Aug-26 08:00 A	21-Sep-26 08:48 A	0.00	0.00	0.00	100%	100%	-20
LANDSCAPE DRAWINGS		39	26-Feb-26 08:00	18-Apr-26 10:00	26-Feb-26 08:00 A	16-Apr-26 17:00 A	0.00	0.00	0.00	0%	0%	0
PG-Q-EN-LS-SD-AP-10	Hardscape Layout Plan	38	28-Feb-26 08:00	18-Apr-26 10:00	28-Feb-26 08:00 A	16-Apr-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-Q-EN-LS-SD-AP-100	Padel Playground Layout	38	28-Feb-26 08:00	18-Apr-26 10:00	28-Feb-26 08:00 A	16-Apr-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-Q-EN-LS-SD-AP-110	Basketball Playground Layout	38	28-Feb-26 08:00	18-Apr-26 10:00	28-Feb-26 08:00 A	16-Apr-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-Q-EN-LS-SD-AP-120	Playground Details	38	28-Feb-26 08:00	18-Apr-26 10:00	28-Feb-26 08:00 A	16-Apr-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-Q-EN-LS-SD-AP-130	Padel Fence Elevation & Details	39	26-Feb-26 08:00	18-Apr-26 10:00	26-Feb-26 08:00 A	16-Apr-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-Q-EN-LS-SD-AP-20	Interlock Tile Details	28	11-Mar-26 08:00	18-Apr-26 10:00	11-Mar-26 08:00 A	16-Apr-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-Q-EN-LS-SD-AP-30	Stamped Concrete Pattern & Section	18	28-Mar-26 08:00	18-Apr-26 10:00	28-Mar-26 08:00 A	16-Apr-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-Q-EN-LS-SD-AP-40	Tartan Flooring Layout & Details	38	28-Feb-26 08:00	18-Apr-26 10:00	28-Feb-26 08:00 A	16-Apr-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-Q-EN-LS-SD-AP-50	Bike Path Layout & Details	39	26-Feb-26 08:00	18-Apr-26 10:00	26-Feb-26 08:00 A	16-Apr-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-Q-EN-LS-SD-AP-60	Walking Path layout & Details	39	26-Feb-26 08:00	18-Apr-26 10:00	26-Feb-26 08:00 A	16-Apr-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-Q-EN-LS-SD-AP-70	Tree Planting Plan & Details	38	28-Feb-26 08:00	18-Apr-26 10:00	28-Feb-26 08:00 A	16-Apr-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-Q-EN-LS-SD-AP-80	Traffic Sign Location & Details	39	26-Feb-26 08:00	18-Apr-26 10:00	26-Feb-26 08:00 A	16-Apr-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-Q-EN-LS-SD-AP-90	Football Playground Layout	38	28-Feb-26 08:00	18-Apr-26 10:00	28-Feb-26 08:00 A	16-Apr-26 17:00 A	0.00	0.00	0.00	100%	100%	0
MECHANICAL DRAWINGS		154	09-Mar-26 08:00	27-Jul-26 17:00	09-Mar-26 08:00 A	21-Sep-26 08:48 A	0.00	0.00	0.00	0%	0%	-47
WATER SUPPLY SYSTEM		27	09-Mar-26 08:00	14-Apr-26 10:00	09-Mar-26 08:00 A	13-Apr-26 17:00 A	0.00	0.00	0.00	0%	0%	0
PG-Q-EN-ME-SD-AP-10	Cold & Hot Water Piping Layout	27	09-Mar-26 08:00	14-Apr-26 10:00	09-Mar-26 08:00 A	13-Apr-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-Q-EN-ME-SD-AP-20	Pump Room Layout	21	16-Mar-26 08:00	14-Apr-26 10:00	16-Mar-26 08:00 A	13-Apr-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-Q-EN-ME-SD-AP-30	Booster Pump Details	26	10-Mar-26 08:00	14-Apr-26 10:00	10-Mar-26 08:00 A	13-Apr-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-Q-EN-ME-SD-AP-40	GRP Water Tank Details	22	14-Mar-26 08:00	13-Apr-26 10:36	14-Mar-26 08:00 A	13-Apr-26 09:36 A	0.00	0.00	0.00	100%	100%	0
SEWER AND DRAINAGE SYSTEM		27	09-Mar-26 08:00	14-Apr-26 10:00	09-Mar-26 08:00 A	13-Apr-26 17:00 A	0.00	0.00	0.00	0%	0%	0
PG-Q-EN-ME-SD-AP-50	Drainage Layout	27	09-Mar-26 08:00	14-Apr-26 10:00	09-Mar-26 08:00 A	13-Apr-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-Q-EN-ME-SD-AP-60	Floor Drains & Cleanouts Details	21	16-Mar-26 08:00	14-Apr-26 10:00	16-Mar-26 08:00 A	13-Apr-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-Q-EN-ME-SD-AP-70	Inspection Chamber Details	21	16-Mar-26 08:00	14-Apr-26 10:00	16-Mar-26 08:00 A	13-Apr-26 17:00 A	0.00	0.00	0.00	100%	100%	0
IRRIGATION SYSTEM		24	12-Mar-26 08:00	14-Apr-26 10:00	12-Mar-26 08:00 A	13-Apr-26 17:00 A	0.00	0.00	0.00	0%	0%	0
PG-Q-EN-ME-SD-AP-80	HDPE Pipe Routing	24	12-Mar-26 08:00	14-Apr-26 10:00	12-Mar-26 08:00 A	13-Apr-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-Q-EN-ME-SD-AP-90	Irrigation Network Layout	20	17-Mar-26 08:00	14-Apr-26 10:00	17-Mar-26 08:00 A	13-Apr-26 17:00 A	0.00	0.00	0.00	100%	100%	0
AIR DOME		10	16-Jul-26 08:00	27-Jul-26 17:00	20-Aug-26 08:00 A	21-Sep-26 08:48 A	0.00	0.00	0.00	0%	0%	-17
PG-Q-EN-ME-SD-AP-100	Air Package and HVAC System Drawings	10	16-Jul-26 08:00	27-Jul-26 17:00	20-Aug-26 08:00 A	21-Sep-26 08:48 A	0.00	0.00	0.00	100%	100%	-17
ELECTRICAL DRAWINGS		100	20-May-26 08:00	16-Aug-26 17:00	20-May-26 08:00 A	21-Sep-26 08:48 A	0.00	0.00	0.00	0%	0%	-30
POWER AND LIGHTING SYSTEM		20	20-May-26 08:00	17-Jun-26 10:00	20-May-26 08:00 A	16-Jun-26 17:00 A	0.00	0.00	0.00	0%	0%	0
PG-Q-EN-EL-SD-AP-10	Main Distribution Board (MDB) Layout	20	20-May-26 08:00	17-Jun-26 10:00	20-May-26 08:00 A	16-Jun-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-Q-EN-EL-SD-AP-20	Pump Room Power Panel	20	20-May-26 08:00	17-Jun-26 10:00	20-May-26 08:00 A	16-Jun-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-Q-EN-EL-SD-AP-30	Street Lighting Power Panel	20	20-May-26 08:00	17-Jun-26 10:00	20-May-26 08:00 A	16-Jun-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-Q-EN-EL-SD-AP-40	Site Lighting Pole Layout	20	20-May-26 08:00	17-Jun-26 10:00	20-May-26 08:00 A	16-Jun-26 17:00 A	0.00	0.00	0.00	100%	100%	0
ELV SYSTEM		20	20-May-26 08:00	17-Jun-26 10:00	20-May-26 08:00 A	16-Jun-26 17:00 A	0.00	0.00	0.00	0%	0%	0
PG-Q-EN-EL-SD-AP-50	Telecom & Data Layout	20	20-May-26 08:00	17-Jun-26 10:00	20-May-26 08:00 A	16-Jun-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-Q-EN-EL-SD-AP-60	CCTV Camera Layout	20	20-May-26 08:00	17-Jun-26 10:00	20-May-26 08:00 A	16-Jun-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-Q-EN-EL-SD-AP-70	Access Control Layout	20	20-May-26 08:00	17-Jun-26 10:00	20-May-26 08:00 A	16-Jun-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-Q-EN-EL-SD-AP-80	AV System Layout	20	20-May-26 08:00	17-Jun-26 10:00	20-May-26 08:00 A	16-Jun-26 17:00 A	0.00	0.00	0.00	100%	100%	0
FIRE ALARM SYSTEM		20	20-May-26 08:00	17-Jun-26 10:00	20-May-26 08:00 A	16-Jun-26 17:00 A	0.00	0.00	0.00	0%	0%	0
PG-Q-EN-EL-SD-AP-100	Detector & Manual Call Point Details	20	20-May-26 08:00	17-Jun-26 10:00	20-May-26 08:00 A	16-Jun-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-Q-EN-EL-SD-AP-110	Control Panel Wiring Diagram	20	20-May-26 08:00	17-Jun-26 10:00	20-May-26 08:00 A	16-Jun-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-Q-EN-EL-SD-AP-90	Fire Alarm Layout	20	20-May-26 08:00	17-Jun-26 10:00	20-May-26 08:00 A	16-Jun-26 17:00 A	0.00	0.00	0.00	100%	100%	0
AIR DOME		17	28-Jul-26 08:00	16-Aug-26 17:00	20-Aug-26 08:00 A	21-Sep-26 08:48 A	0.00	0.00	0.00	0%	0%	-10
PG-Q-EN-EL-SD-AP-120	Power & Lighting System Drawings	17	28-Jul-26 08:00	16-Aug-26 17:00	20-Aug-26 08:00 A	21-Sep-26 08:48 A	0.00	0.00	0.00	100%	100%	-10
PG-Q-EN-EL-SD-AP-130	Generators Details	8	03-Aug-26 08:00	11-Aug-26 17:00	20-Aug-26 08:00 A	21-Sep-26 08:48 A	0.00	0.00	0.00	100%	100%	-19
PG-Q-EN-EL-SD-AP-140	Smart Dome System Drawings	6	05-Aug-26 08:00	11-Aug-26 17:00	20-Aug-26 08:00 A	21-Sep-26 08:48 A	0.00	0.00	0.00	100%	100%	-21
MATERIAL SUBMITTALS		134	17-Feb-26 08:00	16-Jul-26 17:00	17-Feb-26 08:00 A	20-Aug-26 17:00 A	0.00	0.00	0.00	0%	0%	-30
LONG LEAD ITEMS		134	17-Feb-26 08:00	16-Jul-26 17:00	17-Feb-26 08:00 A	20-Aug-26 17:00 A	0.00	0.00	0.00	0%	0%	-30
EXTERNAL / LANDSCAPE WORK		56	25-Feb-26 08:00	06-May-26 10:00	25-Feb-26 08:00 A	05-May-26 17:00 A	0.00	0.00	0.00	0%	0%	0
PG-Q-PR-LL-LS-MS-10	Bike and Walk Path Materials	49	05-Mar-26 08:00	06-May-26 10:00	05-Mar-26 08:00 A	05-May-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-Q-PR-LL-LS-MS-20	Benches, Seats (Rectangular & Circular)	56	25-Feb-26 08:00	06-May-26 10:00	25-Feb-26 08:00 A	05-May-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-Q-PR-LL-LS-MS-30	Fence, gates and accessories	49	05-Mar-26 08:00	06-May-26 10:00	05-Mar-26 08:00 A	05-May-26 17:00 A	0.00	0.00	0.00	100%	100%	0
SPORTS & RECREATIONAL FACILITIES WORK		134	17-Feb-26 08:00	16-Jul-26 17:00	17-Feb-26 08:00 A	20-Aug-26 17:00 A	0.00	0.00	0.00	0%	0%	-30
PG-Q-PR-LL-SPMS-10	Football Playground Materials (Flooring, goal post, nets, paints, etc)	48	07-Mar-26 08:00	06-May-26 10:00	07-Mar-26 08:00 A	05-May-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-Q-PR-LL-SPMS-20	Basketball Playground Materials (Flooring, basketball poll, nets, paints,	48	07-Mar-26 08:00	06-May-26 10:00	07-Mar-26 08:00 A	05-May-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-Q-PR-LL-SPMS-30	Padel Playgound Materials (Flooring, fence, tempered glass, etc)	48	07-Mar-26 08:00	06-May-26 10:00	07-Mar-26 08:00 A	05-May-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-Q-PR-LL-SPMS-40	Tartan Floor	48	07-Mar-26 08:00	06-May-26 10:00	07-Mar-26 08:00 A	05-May-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-Q-PR-LL-SPMS-50	Air Dome Materials(Completed)	101	17-Feb-26 08:00	25-Jun-26 10:00	17-Feb-26 08:00 A	24-Jun-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-Q-PR-LL-SPMS-50_R	Air Dome Materials(Remaining)	19	25-Jun-26 08:00	16-Jul-26 17:00	30-Jun-26 08:00 A	20-Aug-26 17:00 A	0.00	0.00	0.00	100%	100%	-26
CONCRETE WORK		43	04-Mar-26 08:00	28-Apr-26 10:00	04-Mar-26 08:00 A	27-Apr-26 17:00 A	0.00	0.00	0.00	0%	0%	0
PG-Q-PR-LL-CO-MS-10	Autoclaved Aerated Panel	43	04-Mar-26 08:00	28-Apr-26 10:00	04-Mar-26 08:00 A	27-Apr-26 17:00 A	0.00	0.00	0.00	100%	100%	0
METAL WORK		47	09-Mar-26 08:00	07-May-26 10:00	09-Mar-26 08:00 A	06-May-26 17:00 A	0.00	0.00	0.00	0%	0%	0
PG-Q-PR-LL-MT-MS-10	Metal Doors	47	09-Mar-26 08:00	07-May-26 10:00	09-Mar-26 08:00 A	06-May-26 17:00 A	0.00	0.00	0.00	100%	100%	0

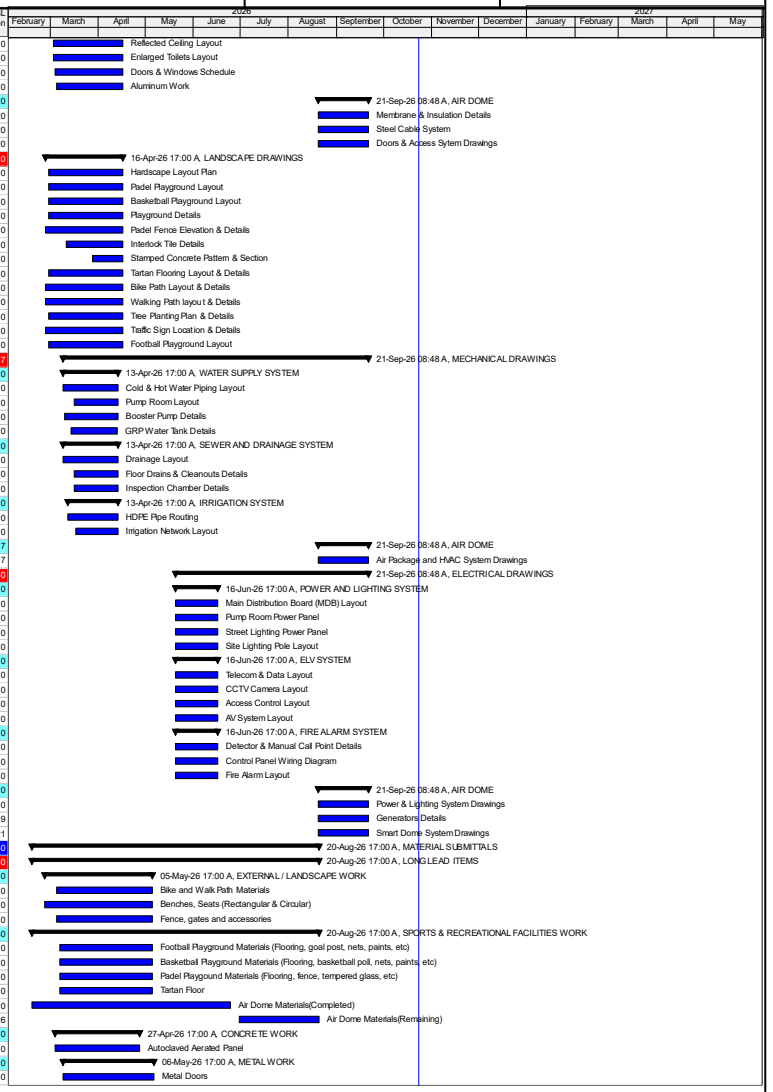


Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining W...
Milestone
summary

Baseline Schedule Rev.00

PLAYGROUNDS INITIATIVE - QASSIM, HAIL & TABUK - 25-Oct-2026

Activity ID	Activity Name	O.D	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Schedule % Complete	Performance % Complete	Variance - BL Project Duration
PG-Q-PR-LL-MT-MS-20	Curtain Wall	47	09-Mar-26 08:00	07-May-26 10:00	09-Mar-26 08:00 A	06-May-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PLUMBING WORK		46	10-Mar-26 08:00	07-May-26 10:00	10-Mar-26 08:00 A	06-May-26 17:00 A	0.00	0.00	0.00	0%	0%	0
PG-Q-PR-LL-PB-MS-10	Booster Pump	46	10-Mar-26 08:00	07-May-26 10:00	10-Mar-26 08:00 A	06-May-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-Q-PR-LL-PB-MS-20	GRP Sectional Panel Water Tanks (4x3x3m)	42	15-Mar-26 08:00	07-May-26 10:00	15-Mar-26 08:00 A	06-May-26 17:00 A	0.00	0.00	0.00	100%	100%	0
IRRIGATION WORK		50	05-Mar-26 08:00	07-May-26 10:00	05-Mar-26 08:00 A	06-May-26 17:00 A	0.00	0.00	0.00	0%	0%	0
PG-Q-PR-LL-IR-MS-10	HDPE Pipes	50	05-Mar-26 08:00	07-May-26 10:00	05-Mar-26 08:00 A	06-May-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-Q-PR-LL-IR-MS-20	Irrigation Control System	50	05-Mar-26 08:00	07-May-26 10:00	05-Mar-26 08:00 A	06-May-26 17:00 A	0.00	0.00	0.00	100%	100%	0
ELECTRICAL WORK		26	12-May-26 08:00	16-Jun-26 10:00	12-May-26 08:00 A	15-Jun-26 17:00 A	0.00	0.00	0.00	0%	0%	0
PG-Q-PR-LL-EL-MS-10	Main Distribution Board	26	12-May-26 08:00	16-Jun-26 10:00	12-May-26 08:00 A	15-Jun-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-Q-PR-LL-EL-MS-20	Power Panels (Pump, Street Light)	26	12-May-26 08:00	16-Jun-26 10:00	12-May-26 08:00 A	15-Jun-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-Q-PR-LL-EL-MS-30	Site Lighting Poles	26	12-May-26 08:00	16-Jun-26 10:00	12-May-26 08:00 A	15-Jun-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-Q-PR-LL-EL-MS-40	Lighting Fixtures	26	12-May-26 08:00	16-Jun-26 10:00	12-May-26 08:00 A	15-Jun-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-Q-PR-LL-EL-MS-50	Grounding System Materials (Earth pit rod, LPS, etc)	26	12-May-26 08:00	16-Jun-26 10:00	12-May-26 08:00 A	15-Jun-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-Q-PR-LL-EL-MS-60	Telecommunications & Data System Materials (Telephone outlet, CCTV,	26	12-May-26 08:00	16-Jun-26 10:00	12-May-26 08:00 A	15-Jun-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-Q-PR-LL-EL-MS-70	Security and Access Control System Materials	26	12-May-26 08:00	16-Jun-26 10:00	12-May-26 08:00 A	15-Jun-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-Q-PR-LL-EL-MS-80	Fire Alarm System Materials	26	12-May-26 08:00	16-Jun-26 10:00	12-May-26 08:00 A	15-Jun-26 17:00 A	0.00	0.00	0.00	100%	100%	0
SHORT LEAD ITEMS		28	17-Feb-26 08:00	28-Mar-26 10:00	17-Feb-26 08:00 A	27-Mar-26 17:00 A	0.00	0.00	0.00	0%	0%	0
EXTERNAL / LANDSCAPE WORK		23	17-Feb-26 08:00	17-Mar-26 10:00	17-Feb-26 08:00 A	16-Mar-26 17:00 A	0.00	0.00	0.00	0%	0%	0
PG-Q-PR-SL-LS-MS-10	Backfilling Materials	23	17-Feb-26 08:00	17-Mar-26 10:00	17-Feb-26 08:00 A	16-Mar-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-Q-PR-SL-LS-MS-20	Interlock tiles	4	12-Mar-26 08:00	17-Mar-26 10:00	12-Mar-26 08:00 A	16-Mar-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-Q-PR-SL-LS-MS-30	Compacted Natural Ground Soil	20	21-Feb-26 08:00	17-Mar-26 10:00	21-Feb-26 08:00 A	16-Mar-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-Q-PR-SL-LS-MS-40	Curb Stone	4	12-Mar-26 08:00	17-Mar-26 10:00	12-Mar-26 08:00 A	16-Mar-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-Q-PR-SL-LS-MS-50	Thermoplastic pavement road marking	4	12-Mar-26 08:00	17-Mar-26 10:00	12-Mar-26 08:00 A	16-Mar-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-Q-PR-SL-LS-MS-60	Traffic Signages	4	12-Mar-26 08:00	17-Mar-26 10:00	12-Mar-26 08:00 A	16-Mar-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-Q-PR-SL-LS-MS-70	Trees	4	12-Mar-26 08:00	17-Mar-26 10:00	12-Mar-26 08:00 A	16-Mar-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-Q-PR-SL-LS-MS-80	Lawn	4	12-Mar-26 08:00	17-Mar-26 10:00	12-Mar-26 08:00 A	16-Mar-26 17:00 A	0.00	0.00	0.00	100%	100%	0
CONCRETE WORK		28	17-Feb-26 08:00	28-Mar-26 10:00	17-Feb-26 08:00 A	27-Mar-26 17:00 A	0.00	0.00	0.00	0%	0%	0
PG-Q-PR-SL-CO-MS-10	Steel Rebar	17	17-Feb-26 08:00	10-Mar-26 10:00	17-Feb-26 08:00 A	09-Mar-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-Q-PR-SL-CO-MS-20	Concrete	13	23-Feb-26 08:00	10-Mar-26 10:00	23-Feb-26 08:00 A	09-Mar-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-Q-PR-SL-CO-MS-30	Screed	9	12-Mar-26 08:00	28-Mar-26 10:00	12-Mar-26 08:00 A	26-Mar-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-Q-PR-SL-CO-MS-40	CMU Block	19	01-Mar-26 08:00	28-Mar-26 09:00	01-Mar-26 08:00 A	27-Mar-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-Q-PR-SL-CO-MS-50	Concrete Repair & Protection Materials	19	01-Mar-26 08:00	28-Mar-26 09:00	01-Mar-26 08:00 A	27-Mar-26 17:00 A	0.00	0.00	0.00	100%	100%	0
ARCHITECTURAL & FINISHES WORK		18	21-Feb-26 08:00	15-Mar-26 10:00	21-Feb-26 08:00 A	14-Mar-26 17:00 A	0.00	0.00	0.00	0%	0%	0
PG-Q-PR-SL-AR-MS-10	Ceramic tiles	4	10-Mar-26 08:00	15-Mar-26 10:00	10-Mar-26 08:00 A	14-Mar-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-Q-PR-SL-AR-MS-100	Gypsum Boards	4	10-Mar-26 08:00	15-Mar-26 10:00	10-Mar-26 08:00 A	14-Mar-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-Q-PR-SL-AR-MS-110	Specialities Materials (Toilet accessories, lockers, logo, etc)	4	10-Mar-26 08:00	15-Mar-26 10:00	10-Mar-26 08:00 A	14-Mar-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-Q-PR-SL-AR-MS-120	Waterproofing System Materials	4	10-Mar-26 08:00	15-Mar-26 10:00	10-Mar-26 08:00 A	14-Mar-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-Q-PR-SL-AR-MS-20	Anti-slip Granite tiles	4	10-Mar-26 08:00	15-Mar-26 10:00	10-Mar-26 08:00 A	14-Mar-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-Q-PR-SL-AR-MS-30	Epoxy Paint	4	10-Mar-26 08:00	15-Mar-26 10:00	10-Mar-26 08:00 A	14-Mar-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-Q-PR-SL-AR-MS-40	Cement Plaster	18	21-Feb-26 08:00	15-Mar-26 10:00	21-Feb-26 08:00 A	14-Mar-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-Q-PR-SL-AR-MS-50	Acrylic Paint	15	25-Feb-26 08:00	15-Mar-26 10:00	25-Feb-26 08:00 A	14-Mar-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-Q-PR-SL-AR-MS-60	Stone Cladding	4	10-Mar-26 08:00	15-Mar-26 10:00	10-Mar-26 08:00 A	14-Mar-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-Q-PR-SL-AR-MS-70	Aluminum Plates	4	10-Mar-26 08:00	15-Mar-26 10:00	10-Mar-26 08:00 A	14-Mar-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-Q-PR-SL-AR-MS-80	Phenolic Partition	10	03-Mar-26 08:00	15-Mar-26 10:00	03-Mar-26 08:00 A	14-Mar-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-Q-PR-SL-AR-MS-90	Glass Partition	10	03-Mar-26 08:00	15-Mar-26 10:00	03-Mar-26 08:00 A	14-Mar-26 17:00 A	0.00	0.00	0.00	100%	100%	0
METAL WORK		11	04-Mar-26 08:00	17-Mar-26 10:00	04-Mar-26 08:00 A	16-Mar-26 17:00 A	0.00	0.00	0.00	0%	0%	0
PG-Q-PR-SL-MT-MS-10	Galvanized Steel Ladder	8	08-Mar-26 08:00	17-Mar-26 10:00	08-Mar-26 08:00 A	16-Mar-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-Q-PR-SL-MT-MS-20	Galvanized Steel Roof Scupper	11	04-Mar-26 08:00	17-Mar-26 10:00	04-Mar-26 08:00 A	16-Mar-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-Q-PR-SL-MT-MS-30	Galvanized Steel Cover with frame	11	04-Mar-26 08:00	17-Mar-26 10:00	04-Mar-26 08:00 A	16-Mar-26 17:00 A	0.00	0.00	0.00	100%	100%	0
HVAC WORK		19	23-Feb-26 08:00	17-Mar-26 10:00	23-Feb-26 08:00 A	16-Mar-26 17:00 A	0.00	0.00	0.00	0%	0%	0
PG-Q-PR-SL-AC-MS-10	Split Air Conditioning Unit	19	23-Feb-26 08:00	17-Mar-26 10:00	23-Feb-26 08:00 A	16-Mar-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-Q-PR-SL-AC-MS-20	Air Duct	15	28-Feb-26 08:00	17-Mar-26 10:00	28-Feb-26 08:00 A	16-Mar-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-Q-PR-SL-AC-MS-30	Diffusers and Grills	11	04-Mar-26 08:00	17-Mar-26 10:00	04-Mar-26 08:00 A	16-Mar-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-Q-PR-SL-AC-MS-40	Exhaust fans	11	04-Mar-26 08:00	17-Mar-26 10:00	04-Mar-26 08:00 A	16-Mar-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PLUMBING WORK		4	12-Mar-26 08:00	17-Mar-26 10:00	12-Mar-26 08:00 A	16-Mar-26 17:00 A	0.00	0.00	0.00	0%	0%	0
PG-Q-PR-SL-PB-MS-10	PPR Pipes & Valves	4	12-Mar-26 08:00	17-Mar-26 10:00	12-Mar-26 08:00 A	16-Mar-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-Q-PR-SL-PB-MS-20	UPCV Pipes	4	12-Mar-26 08:00	17-Mar-26 10:00	12-Mar-26 08:00 A	16-Mar-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-Q-PR-SL-PB-MS-30	Sanitary Drainage Fixtures	4	12-Mar-26 08:00	17-Mar-26 10:00	12-Mar-26 08:00 A	16-Mar-26 17:00 A	0.00	0.00	0.00	100%	100%	0
IRRIGATION WORK		17	25-Feb-26 08:00	17-Mar-26 10:00	25-Feb-26 08:00 A	16-Mar-26 17:00 A	0.00	0.00	0.00	0%	0%	0
PG-Q-PR-SL-IR-MS-10	Gate Valve including valve box	17	25-Feb-26 08:00	17-Mar-26 10:00	25-Feb-26 08:00 A	16-Mar-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-Q-PR-SL-IR-MS-20	Bubblers and Sprayers	12	03-Mar-26 08:00	17-Mar-26 10:00	03-Mar-26 08:00 A	16-Mar-26 17:00 A	0.00	0.00	0.00	100%	100%	0
ELECTRICAL WORK		4	12-Mar-26 08:00	17-Mar-26 10:00	12-Mar-26 08:00 A	16-Mar-26 17:00 A	0.00	0.00	0.00	0%	0%	0
PG-Q-PR-SL-EL-MS-10	Wiring Devices Materials	4	12-Mar-26 08:00	17-Mar-26 10:00	12-Mar-26 08:00 A	16-Mar-26 17:00 A	0.00	0.00	0.00	100%	100%	0
FIRE FIGHTING WORK		4	12-Mar-26 08:00	17-Mar-26 10:00	12-Mar-26 08:00 A	16-Mar-26 17:00 A	0.00	0.00	0.00	0%	0%	0
PG-Q-PR-SL-FF-MS-10	Fire Extinguishers	4	12-Mar-26 08:00	17-Mar-26 10:00	12-Mar-26 08:00 A	16-Mar-26 17:00 A	0.00	0.00	0.00	100%	100%	0
MATERIAL APPROVALS		196	21-Feb-26 08:00	18-Jul-26 17:00	21-Feb-26 08:00 A	01-Oct-26 17:00 A	526,126.20	526,126.20	526,126.20	100%	100%	-64
LONG LEAD ITEMS		189	02-Mar-26 08:00	18-Jul-26 17:00	02-Mar-26 08:00 A	01-Oct-26 17:00 A	358,885.26	358,885.26	358,885.26	100%	100%	-64
EXTERNAL / LANDSCAPE WORK		2	11-May-26 08:00	12-May-26 17:00	11-May-26 08:00 A	12-May-26 17:00 A	19,812.18	19,812.18	19,812.18	100%	100%	0
PG-Q-PR-LL-LS-MA-10	Bike and Walk Path Materials	2	11-May-26 08:00	12-May-26 17:00	11-May-26 08:00 A	12-May-26 17:00 A	13,275.00	13,275.00	13,275.00	100%	100%	0
PG-Q-PR-LL-LS-MA-20	Benches, Seats (Rectangular & Circular)	2	11-May-26 08:00	12-May-26 17:00	11-May-26 08:00 A	12-May-26 17:00 A	4,007.97	4,007.97	4,007.97	100%	100%	0
PG-Q-PR-LL-LS-MA-30	Fence, gates and accessories	2	11-May-26 08:00	12-May-26 17:00	11-May-26 08:00 A	12-May-26 17:00 A	2,529.21	2,529.21	2,529.21	100%	100%	0
SPORTS & RECREATIONAL FACILITIES WORK		110	02-Mar-26 08:00	30-Jun-26 17:00	02-Mar-26 08:00 A	19-Sep-26 12:00 A	273,522.54	273,522.54	273,522.54	100%	100%	-69
PG-Q-PR-LL-SP-MA-10	Football Playground Materials (Flooring, goal post, nets, paints, etc)	8	12-May-26 08:00	20-May-26 17:00	12-May-26 08:00 A	20-May-26 17:00 A	13,051.50	13,051.50	13,051.50	100%	100%	0

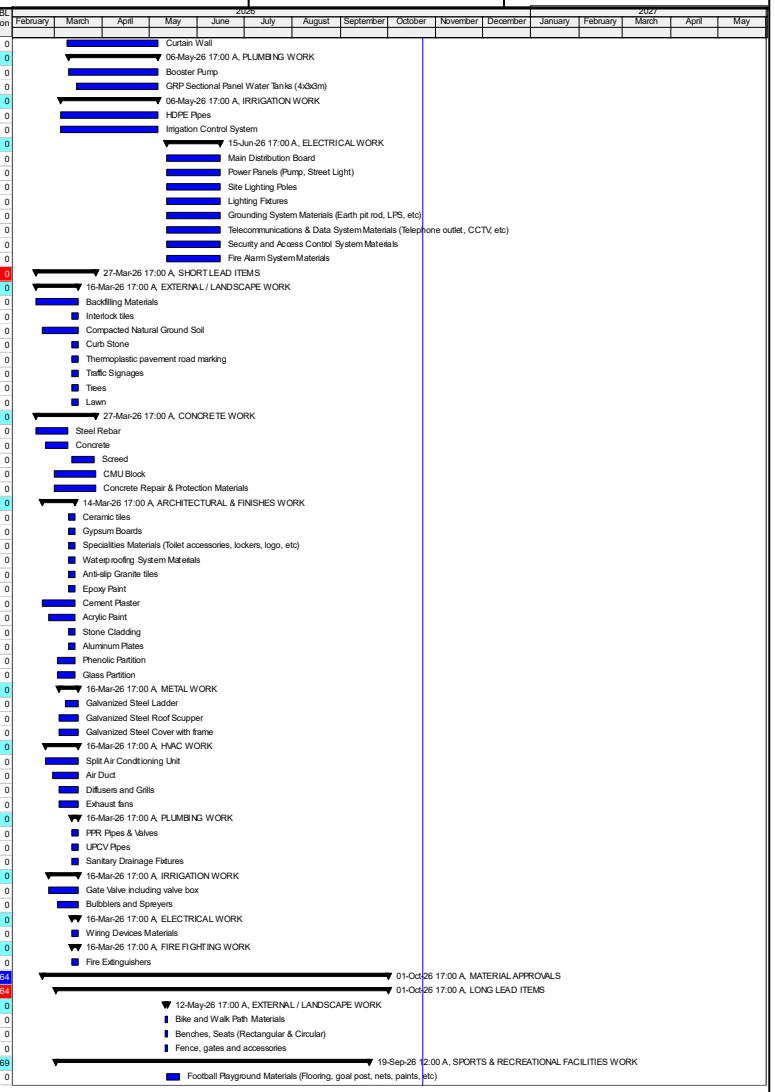


Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining W...
Milestone
summary

Baseline Schedule Rev.00

PLAYGROUNDS INITIATIVE - QASSIM, HAIL & TABUK - 25-Oct-2026

Activity ID	Activity Name	O.D	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Schedule % Complete	Performance % Complete	Variance - BL Project Duration
PG-Q-PR-LL-SP-MA-20	Basketball Playground Materials (Flooring, basketball poll, nets, paints,	8	12-May-26 08:00	20-May-26 17:00	12-May-26 08:00 A	20-May-26 17:00 A	2,256.00	2,256.00	2,256.00	100%	100%	0
PG-Q-PR-LL-SP-MA-30	Padel Playgound Materials (Flooring, fence, tempered glass, etc)	8	12-May-26 08:00	20-May-26 17:00	12-May-26 08:00 A	20-May-26 17:00 A	5,950.80	5,950.80	5,950.80	100%	100%	0
PG-Q-PR-LL-SP-MA-40	Tartan Floor	8	12-May-26 08:00	20-May-26 17:00	12-May-26 08:00 A	20-May-26 17:00 A	43,524.00	43,524.00	43,524.00	100%	100%	0
PG-Q-PR-LL-SP-MA-50	Air Dome Materials(Completed)	91	02-Mar-26 08:00	24-Jun-26 17:00	02-Mar-26 08:00 A	24-Jun-26 17:00 A	62,622.07	62,622.07	62,622.07	100%	100%	0
PG-Q-PR-LL-SP-MA-50_R	Air Dome Materials(Remaining)	5	25-Jun-26 08:00	30-Jun-26 17:00	02-Jul-26 08:00 A	19-Sep-26 12:00 A	146,118.17	146,118.17	146,118.17	100%	100%	-63
CONCRETE WORK		40	09-Mar-26 08:00	28-Apr-26 17:00	09-Mar-26 08:00 A	28-Apr-26 17:00 A	1,417.50	1,417.50	1,417.50	100%	100%	0
PG-Q-PR-LL-CO-MA-10	Autoclaved Aerated Panel	40	09-Mar-26 08:00	28-Apr-26 17:00	09-Mar-26 08:00 A	28-Apr-26 17:00 A	1,417.50	1,417.50	1,417.50	100%	100%	0
METAL WORK		112	09-Jun-26 08:00	18-Jul-26 17:00	09-Jun-26 08:00 A	01-Oct-26 17:00 A	889.23	889.23	889.23	100%	100%	-64
PG-Q-PR-LL-MT-MA-10	Metal Doors(Completed)	14	09-Jun-26 08:00	24-Jun-26 17:00	09-Jun-26 08:00 A	24-Jun-26 17:00 A	76.52	76.52	76.52	100%	100%	0
PG-Q-PR-LL-MT-MA-10_R	Metal Doors(Remaining)	15	25-Jun-26 08:00	12-Jul-26 17:00	16-Sep-26 08:00 A	01-Oct-26 17:00 A	51.01	51.01	51.01	100%	100%	2
PG-Q-PR-LL-MT-MA-20	Curtain Wall(Completed)	14	09-Jun-26 08:00	24-Jun-26 17:00	09-Jun-26 08:00 A	24-Jun-26 17:00 A	457.02	457.02	457.02	100%	100%	0
PG-Q-PR-LL-MT-MA-20_R	Curtain Wall(Remaining)	20	25-Jun-26 08:00	18-Jul-26 17:00	16-Sep-26 08:00 A	01-Oct-26 17:00 A	304.68	304.68	304.68	100%	100%	7
PLUMBING WORK		48	09-Jun-26 08:00	18-Jul-26 17:00	20-May-26 08:00 A	24-Jun-26 17:00 A	3,553.95	3,553.95	3,553.95	100%	100%	7
PG-Q-PR-LL-PB-MA-10	Booster Pump(Completed)	14	09-Jun-26 08:00	24-Jun-26 17:00	09-Jun-26 08:00 A	24-Jun-26 17:00 A	1,090.98	1,090.98	1,090.98	100%	100%	0
PG-Q-PR-LL-PB-MA-10_R	Booster Pump(Remaining)	20	25-Jun-26 08:00	18-Jul-26 17:00	20-May-26 08:00 A	21-May-26 17:00 A	727.32	727.32	727.32	100%	100%	18
PG-Q-PR-LL-PB-MA-20	GRP Sectional Panel Water Tanks (4x3x3m)(Completed)	14	09-Jun-26 08:00	24-Jun-26 17:00	09-Jun-26 08:00 A	24-Jun-26 17:00 A	1,041.39	1,041.39	1,041.39	100%	100%	0
PG-Q-PR-LL-PB-MA-20_R	GRP Sectional Panel Water Tanks (4x3x3m)(Remaining)	15	25-Jun-26 08:00	12-Jul-26 17:00	03-Jun-26 08:00 A	06-Jun-26 17:00 A	694.26	694.26	694.26	100%	100%	12
IRRIGATION WORK		45	11-Mar-26 08:00	06-May-26 17:00	11-Mar-26 08:00 A	06-May-26 17:00 A	24,486.75	24,486.75	24,486.75	100%	100%	0
PG-Q-PR-LL-IR-MA-10	HDPE Pipes	45	11-Mar-26 08:00	06-May-26 17:00	11-Mar-26 08:00 A	06-May-26 17:00 A	19,941.00	19,941.00	19,941.00	100%	100%	0
PG-Q-PR-LL-IR-MA-20	Irrigation Control System	45	11-Mar-26 08:00	06-May-26 17:00	11-Mar-26 08:00 A	06-May-26 17:00 A	4,545.75	4,545.75	4,545.75	100%	100%	0
ELECTRICAL WORK		96	12-May-26 08:00	02-Jul-26 17:00	12-May-26 08:00 A	16-Sep-26 08:24 A	35,203.11	35,203.11	35,203.11	100%	100%	-64
PG-Q-PR-LL-EL-MA-10	Main Distribution Board(Completed)	34	12-May-26 08:00	24-Jun-26 17:00	12-May-26 08:00 A	24-Jun-26 17:00 A	297.54	297.54	297.54	100%	100%	0
PG-Q-PR-LL-EL-MA-10_R	Main Distribution Board(Remaining)	7	25-Jun-26 08:00	02-Jul-26 17:00	30-Jul-26 08:00 A	16-Sep-26 08:24 A	198.36	198.36	198.36	100%	100%	-34
PG-Q-PR-LL-EL-MA-20	Power Panels (Pump, Street Light)(Completed)	34	12-May-26 08:00	24-Jun-26 17:00	12-May-26 08:00 A	24-Jun-26 17:00 A	238.03	238.03	238.03	100%	100%	0
PG-Q-PR-LL-EL-MA-20_R	Power Panels (Pump, Street Light)(Remaining)	7	25-Jun-26 08:00	02-Jul-26 17:00	30-Jul-26 08:00 A	16-Sep-26 08:24 A	158.69	158.69	158.69	100%	100%	-34
PG-Q-PR-LL-EL-MA-30	Site Lighting Poles(Completed)	34	12-May-26 08:00	24-Jun-26 17:00	12-May-26 08:00 A	24-Jun-26 17:00 A	17,405.28	17,405.28	17,405.28	100%	100%	0
PG-Q-PR-LL-EL-MA-30_R	Site Lighting Poles(Remaining)	7	25-Jun-26 08:00	02-Jul-26 17:00	30-Jul-26 08:00 A	16-Sep-26 08:24 A	11,603.52	11,603.52	11,603.52	100%	100%	-34
PG-Q-PR-LL-EL-MA-40	Lighting Fixtures(Completed)	34	12-May-26 08:00	24-Jun-26 17:00	12-May-26 08:00 A	24-Jun-26 17:00 A	769.70	769.70	769.70	100%	100%	0
PG-Q-PR-LL-EL-MA-40_R	Lighting Fixtures(Remaining)	7	25-Jun-26 08:00	02-Jul-26 17:00	12-Jul-26 08:00 A	23-Jul-26 17:00 A	513.13	513.13	513.13	100%	100%	-4
PG-Q-PR-LL-EL-MA-50	Grounding System Materials (Earth pit rod, LPS, etc)(Completed)	34	12-May-26 08:00	24-Jun-26 17:00	12-May-26 08:00 A	24-Jun-26 17:00 A	602.51	602.51	602.51	100%	100%	0
PG-Q-PR-LL-EL-MA-50_R	Grounding System Materials (Earth pit rod, LPS, etc)(Remaining)	7	25-Jun-26 08:00	02-Jul-26 17:00	30-Jul-26 08:00 A	16-Sep-26 08:24 A	401.68	401.68	401.68	100%	100%	-34
PG-Q-PR-LL-EL-MA-60	Telecommunications & Data System Materials (Telephone outlet, CCTV,	34	12-May-26 08:00	24-Jun-26 17:00	12-May-26 08:00 A	24-Jun-26 17:00 A	587.63	587.63	587.63	100%	100%	0
PG-Q-PR-LL-EL-MA-60_R	Telecommunications & Data System Materials (Telephone outlet, CCTV,	7	25-Jun-26 08:00	02-Jul-26 17:00	30-Jul-26 08:00 A	16-Sep-26 08:24 A	391.75	391.75	391.75	100%	100%	-34
PG-Q-PR-LL-EL-MA-70	Security and Access Control System Materials(Completed)	34	12-May-26 08:00	24-Jun-26 17:00	12-May-26 08:00 A	24-Jun-26 17:00 A	743.94	743.94	743.94	100%	100%	0
PG-Q-PR-LL-EL-MA-70_R	Security and Access Control System Materials(Remaining)	7	25-Jun-26 08:00	02-Jul-26 17:00	27-Aug-26 08:00 A	16-Sep-26 08:24 A	495.96	495.96	495.96	100%	100%	-10
PG-Q-PR-LL-EL-MA-80	Fire Alarm System Materials(Completed)	34	12-May-26 08:00	24-Jun-26 17:00	12-May-26 08:00 A	24-Jun-26 17:00 A	477.23	477.23	477.23	100%	100%	0
PG-Q-PR-LL-EL-MA-80_R	Fire Alarm System Materials(Remaining)	7	25-Jun-26 08:00	02-Jul-26 17:00	27-Aug-26 08:00 A	16-Sep-26 08:24 A	318.16	318.16	318.16	100%	100%	-10
SHORT LEAD ITEMS		25	21-Feb-26 08:00	26-Mar-26 17:00	21-Feb-26 08:00 A	26-Mar-26 17:00 A	167,240.94	167,240.94	167,240.94	100%	100%	0
EXTERNAL / LANDSCAPE WORK		25	21-Feb-26 08:00	26-Mar-26 17:00	21-Feb-26 08:00 A	26-Mar-26 17:00 A	139,867.29	139,867.29	139,867.29	100%	100%	0
PG-Q-PR-SL-LS-MA-10	Backfilling Materials	25	21-Feb-26 08:00	26-Mar-26 17:00	21-Feb-26 08:00 A	26-Mar-26 17:00 A	36,450.00	36,450.00	36,450.00	100%	100%	0
PG-Q-PR-SL-LS-MA-20	Interlock tiles	2	25-Mar-26 08:00	26-Mar-26 17:00	25-Mar-26 08:00 A	26-Mar-26 17:00 A	29,832.00	29,832.00	29,832.00	100%	100%	0
PG-Q-PR-SL-LS-MA-30	Compacted Natural Ground Soil	22	25-Feb-26 08:00	26-Mar-26 17:00	25-Feb-26 08:00 A	26-Mar-26 17:00 A	8,580.00	8,580.00	8,580.00	100%	100%	0
PG-Q-PR-SL-LS-MA-40	Curb Stone	2	25-Mar-26 08:00	26-Mar-26 17:00	25-Mar-26 08:00 A	26-Mar-26 17:00 A	43,185.00	43,185.00	43,185.00	100%	100%	0
PG-Q-PR-SL-LS-MA-50	Thermoplastic pavement road marking	2	25-Mar-26 08:00	26-Mar-26 17:00	25-Mar-26 08:00 A	26-Mar-26 17:00 A	525.63	525.63	525.63	100%	100%	0
PG-Q-PR-SL-LS-MA-60	Traffic Signages	2	25-Mar-26 08:00	26-Mar-26 17:00	25-Mar-26 08:00 A	26-Mar-26 17:00 A	198.36	198.36	198.36	100%	100%	0
PG-Q-PR-SL-LS-MA-70	Trees	2	25-Mar-26 08:00	26-Mar-26 17:00	25-Mar-26 08:00 A	26-Mar-26 17:00 A	9,546.30	9,546.30	9,546.30	100%	100%	0
PG-Q-PR-SL-LS-MA-80	Lawn	2	25-Mar-26 08:00	26-Mar-26 17:00	25-Mar-26 08:00 A	26-Mar-26 17:00 A	11,550.00	11,550.00	11,550.00	100%	100%	0
CONCRETE WORK		24	23-Feb-26 08:00	26-Mar-26 17:00	23-Feb-26 08:00 A	26-Mar-26 17:00 A	1,609.47	1,609.47	1,609.47	100%	100%	0
PG-Q-PR-SL-CO-MA-10	Steel Rebar	14	23-Feb-26 08:00	10-Mar-26 17:00	23-Feb-26 08:00 A	10-Mar-26 17:00 A	476.82	476.82	476.82	100%	100%	0
PG-Q-PR-SL-CO-MA-20	Concrete	9	01-Mar-26 08:00	10-Mar-26 17:00	01-Mar-26 08:00 A	10-Mar-26 17:00 A	518.85	518.85	518.85	100%	100%	0
PG-Q-PR-SL-CO-MA-30	Screed	1	26-Mar-26 08:00	26-Mar-26 17:00	26-Mar-26 08:00 A	26-Mar-26 17:00 A	117.60	117.60	117.60	100%	100%	0
PG-Q-PR-SL-CO-MA-40	CMU Block	15	05-Mar-26 08:00	26-Mar-26 17:00	05-Mar-26 08:00 A	26-Mar-26 17:00 A	124.20	124.20	124.20	100%	100%	0
PG-Q-PR-SL-CO-MA-50	Concrete Repair & Protection Materials	15	05-Mar-26 08:00	26-Mar-26 17:00	05-Mar-26 08:00 A	26-Mar-26 17:00 A	372.00	372.00	372.00	100%	100%	0
ARCHITECTURAL & FINISHES WORK		17	25-Feb-26 08:00	16-Mar-26 17:00	25-Feb-26 08:00 A	16-Mar-26 17:00 A	7,931.55	7,931.55	7,931.55	100%	100%	0
PG-Q-PR-SL-AR-MA-10	Ceramic tiles	2	15-Mar-26 08:00	16-Mar-26 17:00	15-Mar-26 08:00 A	16-Mar-26 17:00 A	571.95	571.95	571.95	100%	100%	0
PG-Q-PR-SL-AR-MA-100	Gypsum Boards	2	15-Mar-26 08:00	16-Mar-26 17:00	15-Mar-26 08:00 A	16-Mar-26 17:00 A	188.58	188.58	188.58	100%	100%	0
PG-Q-PR-SL-AR-MA-110	Specialities Materials (Toilet accessories, lockers, logo, etc)	2	15-Mar-26 08:00	16-Mar-26 17:00	15-Mar-26 08:00 A	16-Mar-26 17:00 A	2,262.87	2,262.87	2,262.87	100%	100%	0
PG-Q-PR-SL-AR-MA-120	Waterproofing System Materials	2	15-Mar-26 08:00	16-Mar-26 17:00	15-Mar-26 08:00 A	16-Mar-26 17:00 A	544.20	544.20	544.20	100%	100%	0
PG-Q-PR-SL-AR-MA-20	Anti-slip Granite tiles	2	15-Mar-26 08:00	16-Mar-26 17:00	15-Mar-26 08:00 A	16-Mar-26 17:00 A	535.50	535.50	535.50	100%	100%	0
PG-Q-PR-SL-AR-MA-30	Epoxy Paint	2	15-Mar-26 08:00	16-Mar-26 17:00	15-Mar-26 08:00 A	16-Mar-26 17:00 A	111.18	111.18	111.18	100%	100%	0
PG-Q-PR-SL-AR-MA-40	Cement Plaster	17	25-Feb-26 08:00	16-Mar-26 17:00	25-Feb-26 08:00 A	16-Mar-26 17:00 A	221.37	221.37	221.37	100%	100%	0
PG-Q-PR-SL-AR-MA-50	Acrylic Paint	14	01-Mar-26 08:00	16-Mar-26 17:00	01-Mar-26 08:00 A	16-Mar-26 17:00 A	147.90	147.90	147.90	100%	100%	0
PG-Q-PR-SL-AR-MA-60	Stone Cladding	2	15-Mar-26 08:00	16-Mar-26 17:00	15-Mar-26 08:00 A	16-Mar-26 17:00 A	1,852.20	1,852.20	1,852.20	100%	100%	0
PG-Q-PR-SL-AR-MA-70	Aluminum Plates	2	15-Mar-26 08:00	16-Mar-26 17:00	15-Mar-26 08:00 A	16-Mar-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-Q-PR-SL-AR-MA-80	Phenolic Partition	2	15-Mar-26 08:00	16-Mar-26 17:00	15-Mar-26 08:00 A	16-Mar-26 17:00 A	1,340.40	1,340.40	1,340.40	100%	100%	0
PG-Q-PR-SL-AR-MA-90	Glass Partition	2	15-Mar-26 08:00	16-Mar-26 17:00	15-Mar-26 08:00 A	16-Mar-26 17:00 A	155.40	155.40	155.40	100%	100%	0
METAL WORK		12	09-Mar-26 08:00	26-Mar-26 17:00	09-Mar-26 08:00 A	26-Mar-26 17:00 A	478.89	478.89	478.89	100%	100%	0
PG-Q-PR-SL-MT-MA-10	Galvanized Steel Ladder	9	12-Mar-26 08:00	26-Mar-26 17:00	12-Mar-26 08:00 A	26-Mar-26 17:00 A	361.86	361.86	361.86	100%	100%	0
PG-Q-PR-SL-MT-MA-20	Galvanized Steel Roof Scupper	12	09-Mar-26 08:00	26-Mar-26 17:00	09-Mar-26 08:00 A	26-Mar-26 17:00 A	31.32	31.32	31.32	100%	100%	0
PG-Q-PR-SL-MT-MA-30	Galvanized Steel Cover with frame	12	09-Mar-26 08:00	26-Mar-26 17:00	09-Mar-26 08:00 A	26-Mar-26 17:00 A	85.71	85.71	85.71	100%	100%	0
HVAC WORK		20	28-Feb-26 08:00	26-Mar-26 17:00	28-Feb-26 08:00 A	26-Mar-26 17:00 A	606.36	606.36	606.36	100%	100%	0
PG-Q-PR-SL-AC-MA-10	Split Air Conditioning Unit	20	28-Feb-26 08:00	26-Mar-26 17:00	28-Feb-26 08:00 A	26-Mar-26 17:00 A	309.93	309.93	309.93	100%	100%	0
PG-Q-PR-SL-AC-MA-20	Air Duct	16	04-Mar-26 08:00	26-Mar-26 17:00	04-Mar-26 08:00 A	26-Mar-26 17:00 A	156.00	156.00	156.00	100%	100%	0

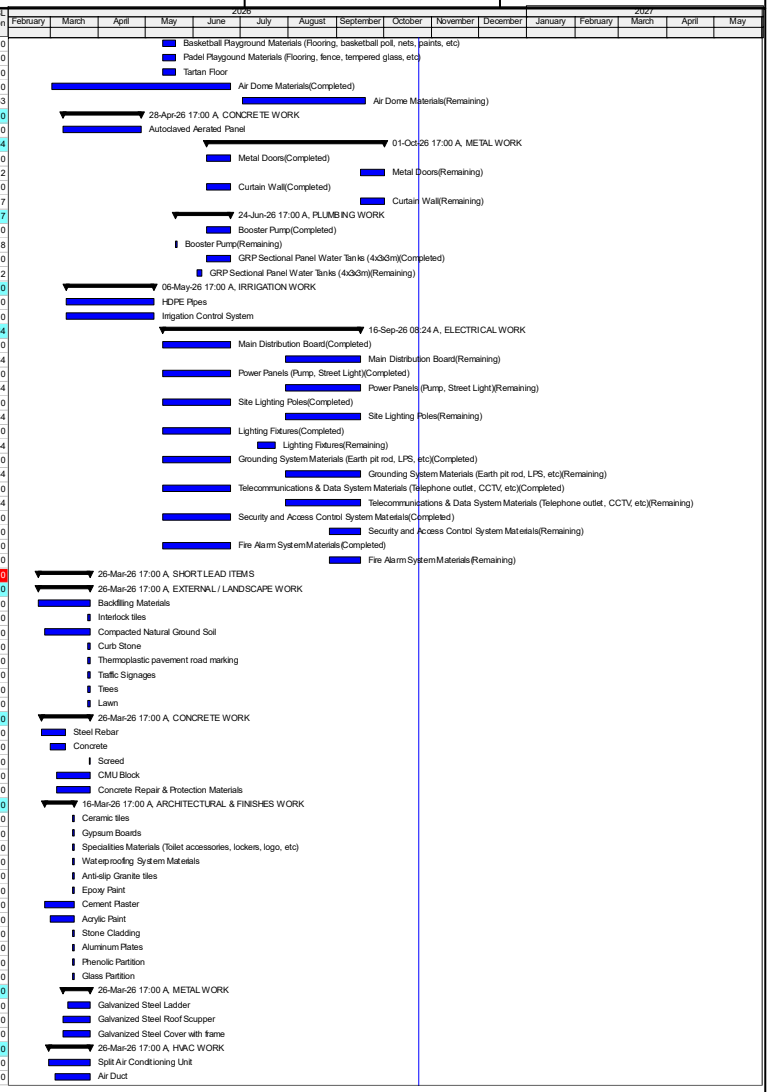


Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining W...
Milestone
summary

Baseline Schedule Rev.00

PLAYGROUNDS INITIATIVE - QASSIM, HAIL & TABUK - 25-Oct-2026

Activity ID	Activity Name	O.D	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Schedule % Complete	Performance % Complete	Variance - BL Project Duration
PG-Q-PR-SL-AC-MA-30	Diffusers and Grills	11	10-Mar-26 08:00	26-Mar-26 17:00	10-Mar-26 08:00 A	26-Mar-26 17:00 A	74.31	74.31	74.31	100%	100%	0
PG-Q-PR-SL-AC-MA-40	Exhaust fans	11	10-Mar-26 08:00	26-Mar-26 17:00	10-Mar-26 08:00 A	26-Mar-26 17:00 A	66.12	66.12	66.12	100%	100%	0
PLUMBING WORK		2	25-Mar-26 08:00	26-Mar-26 17:00	25-Mar-26 08:00 A	26-Mar-26 17:00 A	3,147.03	3,147.03	3,147.03	100%	100%	0
PG-Q-PR-SL-PB-MA-10	PPR Pipes & Valves	2	25-Mar-26 08:00	26-Mar-26 17:00	25-Mar-26 08:00 A	26-Mar-26 17:00 A	265.20	265.20	265.20	100%	100%	0
PG-Q-PR-SL-PB-MA-20	UPCV Pipes	2	25-Mar-26 08:00	26-Mar-26 17:00	25-Mar-26 08:00 A	26-Mar-26 17:00 A	335.19	335.19	335.19	100%	100%	0
PG-Q-PR-SL-PB-MA-30	Sanitary Drainage Fixtures	2	25-Mar-26 08:00	26-Mar-26 17:00	25-Mar-26 08:00 A	26-Mar-26 17:00 A	2,546.64	2,546.64	2,546.64	100%	100%	0
IRRIGATION WORK		17	03-Mar-26 08:00	26-Mar-26 17:00	03-Mar-26 08:00 A	26-Mar-26 17:00 A	13,170.12	13,170.12	13,170.12	100%	100%	0
PG-Q-PR-SL-IR-MA-10	Gate Valve including valve box	17	03-Mar-26 08:00	26-Mar-26 17:00	03-Mar-26 08:00 A	26-Mar-26 17:00 A	1,330.74	1,330.74	1,330.74	100%	100%	0
PG-Q-PR-SL-IR-MA-20	Bubblers and Sprayers	12	09-Mar-26 08:00	26-Mar-26 17:00	09-Mar-26 08:00 A	26-Mar-26 17:00 A	11,839.38	11,839.38	11,839.38	100%	100%	0
ELECTRICAL WORK		2	25-Mar-26 08:00	26-Mar-26 17:00	25-Mar-26 08:00 A	26-Mar-26 17:00 A	407.52	407.52	407.52	100%	100%	0
PG-Q-PR-SL-EL-MA-10	Wiring Devices Materials	2	25-Mar-26 08:00	26-Mar-26 17:00	25-Mar-26 08:00 A	26-Mar-26 17:00 A	407.52	407.52	407.52	100%	100%	0
FIRE FIGHTING WORK		2	25-Mar-26 08:00	26-Mar-26 17:00	25-Mar-26 08:00 A	26-Mar-26 17:00 A	22.71	22.71	22.71	100%	100%	0
PG-Q-PR-SL-FF-MA-10	Fire Extinguishers	2	25-Mar-26 08:00	26-Mar-26 17:00	25-Mar-26 08:00 A	26-Mar-26 17:00 A	22.71	22.71	22.71	100%	100%	0
PROCUREMENT		226	03-Mar-26 08:00	27-Aug-26 17:00	03-Mar-26 08:00 A	28-Oct-26 12:00	4,735,135.80	4,306,400.85	4,735,135.80	100%	90.95%	-52
LONG LEAD ITEMS		213	18-Mar-26 08:00	27-Aug-26 17:00	18-Mar-26 08:00 A	28-Oct-26 12:00	3,229,967.34	2,816,604.28	3,229,967.34	100%	87.2%	-52
PURCHASE ORDER		147	18-Mar-26 08:00	12-Jul-26 17:00	18-Mar-26 08:00 A	16-Sep-26 12:48 A	0.00	0.00	0.00	0%	0%	-57
EXTERNAL / LANDSCAPE WORK		5	06-May-26 08:00	12-May-26 10:00	06-May-26 08:00 A	11-May-26 17:00 A	0.00	0.00	0.00	0%	0%	0
PG-Q-PR-LL-LS-PO-10	Bike and Walk Path Materials	5	06-May-26 08:00	12-May-26 10:00	06-May-26 08:00 A	11-May-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-Q-PR-LL-LS-PO-20	Benches, Seats (Rectangular & Circular)	5	06-May-26 08:00	12-May-26 10:00	06-May-26 08:00 A	11-May-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-Q-PR-LL-LS-PO-30	Fence, gates and accessories	5	06-May-26 08:00	12-May-26 10:00	06-May-26 08:00 A	11-May-26 17:00 A	0.00	0.00	0.00	100%	100%	0
SPORTS & RECREATIONAL FACILITIES WORK		101	26-Mar-26 08:00	09-Jul-26 17:00	26-Mar-26 08:00 A	09-Jul-26 17:00 A	0.00	0.00	0.00	0%	0%	0
PG-Q-PR-LL-SP-PO-10	Football Playground Materials (Flooring, goal post, nets, paints, etc)	35	28-Mar-26 08:00	07-May-26 10:00	28-Mar-26 08:00 A	06-May-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-Q-PR-LL-SP-PO-20	Basketball Playground Materials (Flooring, basketball poll, nets, paints,	35	28-Mar-26 08:00	07-May-26 10:00	28-Mar-26 08:00 A	06-May-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-Q-PR-LL-SP-PO-30	Padel Playgound Materials (Flooring, fence, tempered glass, etc)	35	28-Mar-26 08:00	07-May-26 10:00	28-Mar-26 08:00 A	06-May-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-Q-PR-LL-SP-PO-40	Tartan Floor	36	26-Mar-26 08:00	07-May-26 10:00	26-Mar-26 08:00 A	06-May-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-Q-PR-LL-SP-PO-50	Air Dome Materials	8	01-Jul-26 08:00	09-Jul-26 17:00	08-Jul-26 08:00 A	09-Jul-26 17:00 A	0.00	0.00	0.00	100%	100%	6
CONCRETE WORK		39	18-Mar-26 08:00	07-May-26 10:00	18-Mar-26 08:00 A	06-May-26 17:00 A	0.00	0.00	0.00	0%	0%	0
PG-Q-PR-LL-CO-PO-10	Autoclaved Aerated Panel	39	18-Mar-26 08:00	07-May-26 10:00	18-Mar-26 08:00 A	06-May-26 17:00 A	0.00	0.00	0.00	100%	100%	0
METAL WORK		36	26-Mar-26 08:00	07-May-26 10:00	26-Mar-26 08:00 A	06-May-26 17:00 A	0.00	0.00	0.00	0%	0%	0
PG-Q-PR-LL-MT-PO-10	Metal Doors	36	26-Mar-26 08:00	07-May-26 10:00	26-Mar-26 08:00 A	06-May-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-Q-PR-LL-MT-PO-20	Curtain Wall	36	26-Mar-26 08:00	07-May-26 10:00	26-Mar-26 08:00 A	06-May-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PLUMBING WORK		34	29-Mar-26 08:00	07-May-26 10:00	29-Mar-26 08:00 A	06-May-26 17:00 A	0.00	0.00	0.00	0%	0%	0
PG-Q-PR-LL-PB-PO-10	Booster Pump	34	29-Mar-26 08:00	07-May-26 10:00	29-Mar-26 08:00 A	06-May-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-Q-PR-LL-PB-PO-20	GRP Sectional Panel Water Tanks (4x3x3m)	30	02-Apr-26 08:00	07-May-26 10:00	02-Apr-26 08:00 A	06-May-26 17:00 A	0.00	0.00	0.00	100%	100%	0
IRRIGATION WORK		37	25-Mar-26 08:00	07-May-26 10:00	25-Mar-26 08:00 A	06-May-26 17:00 A	0.00	0.00	0.00	0%	0%	0
PG-Q-PR-LL-IR-PO-10	HDPE Pipes	37	25-Mar-26 08:00	07-May-26 10:00	25-Mar-26 08:00 A	06-May-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-Q-PR-LL-IR-PO-20	Irrigation Control System	37	25-Mar-26 08:00	07-May-26 10:00	25-Mar-26 08:00 A	06-May-26 17:00 A	0.00	0.00	0.00	100%	100%	0
ELECTRICAL WORK		103	13-May-26 08:00	12-Jul-26 17:00	13-May-26 08:00 A	16-Sep-26 12:48 A	0.00	0.00	0.00	0%	0%	-57
PG-Q-PR-LL-EL-PO-10	Main Distribution Board(Completed)	33	13-May-26 08:00	25-Jun-26 10:00	13-May-26 08:00 A	24-Jun-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-Q-PR-LL-EL-PO-10_R	Main Distribution Board(Remaining)	8	04-Jul-26 08:00	12-Jul-26 17:00	14-Aug-26 08:00 A	16-Sep-26 12:48 A	0.00	0.00	0.00	100%	100%	-21
PG-Q-PR-LL-EL-PO-20	Power Panels (Pump, Street Light)(Completed)	33	13-May-26 08:00	25-Jun-26 10:00	13-May-26 08:00 A	24-Jun-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-Q-PR-LL-EL-PO-20_R	Power Panels (Pump, Street Light)(Remaining)	8	04-Jul-26 08:00	12-Jul-26 17:00	14-Aug-26 08:00 A	16-Sep-26 12:48 A	0.00	0.00	0.00	100%	100%	-21
PG-Q-PR-LL-EL-PO-30	Site Lighting Poles(Completed)	33	13-May-26 08:00	25-Jun-26 10:00	13-May-26 08:00 A	24-Jun-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-Q-PR-LL-EL-PO-30_R	Site Lighting Poles(Remaining)	8	04-Jul-26 08:00	12-Jul-26 17:00	14-Aug-26 08:00 A	16-Sep-26 12:48 A	0.00	0.00	0.00	100%	100%	-21
PG-Q-PR-LL-EL-PO-40	Lighting Fixtures(Completed)	33	13-May-26 08:00	25-Jun-26 10:00	13-May-26 08:00 A	24-Jun-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-Q-PR-LL-EL-PO-40_R	Lighting Fixtures(Remaining)	8	04-Jul-26 08:00	12-Jul-26 17:00	23-Jul-26 08:00 A	16-Sep-26 12:48 A	0.00	0.00	0.00	100%	100%	-40
PG-Q-PR-LL-EL-PO-50	Grounding System Materials (Earth pit rod, LPS, etc)(Completed)	33	13-May-26 08:00	25-Jun-26 10:00	13-May-26 08:00 A	24-Jun-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-Q-PR-LL-EL-PO-50_R	Grounding System Materials (Earth pit rod, LPS, etc)(Remaining)	8	04-Jul-26 08:00	12-Jul-26 17:00	27-Aug-26 08:00 A	16-Sep-26 12:48 A	0.00	0.00	0.00	100%	100%	-10
PG-Q-PR-LL-EL-PO-60	Telecommunications & Data System Materials (Telephone outlet, CCTV,	33	13-May-26 08:00	25-Jun-26 10:00	13-May-26 08:00 A	24-Jun-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-Q-PR-LL-EL-PO-60_R	Telecommunications & Data System Materials (Telephone outlet, CCTV,	8	04-Jul-26 08:00	12-Jul-26 17:00	27-Aug-26 08:00 A	16-Sep-26 12:48 A	0.00	0.00	0.00	100%	100%	-10
PG-Q-PR-LL-EL-PO-70	Security and Access Control System Materials(Completed)	33	13-May-26 08:00	25-Jun-26 10:00	13-May-26 08:00 A	24-Jun-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-Q-PR-LL-EL-PO-70_R	Security and Access Control System Materials(Remaining)	8	04-Jul-26 08:00	12-Jul-26 17:00	27-Aug-26 08:00 A	16-Sep-26 12:48 A	0.00	0.00	0.00	100%	100%	-10
PG-Q-PR-LL-EL-PO-80	Fire Alarm System Materials(Completed)	33	13-May-26 08:00	25-Jun-26 10:00	13-May-26 08:00 A	24-Jun-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-Q-PR-LL-EL-PO-80_R	Fire Alarm System Materials(Remaining)	8	04-Jul-26 08:00	12-Jul-26 17:00	27-Aug-26 08:00 A	16-Sep-26 12:48 A	0.00	0.00	0.00	100%	100%	-10
MANUFACTURE / FABRICATION		161	05-May-26 08:00	11-Aug-26 17:00	05-May-26 08:00 A	04-Oct-26 17:00 A	0.00	0.00	0.00	0%	0%	-45
EXTERNAL / LANDSCAPE WORK		109	05-May-26 08:00	23-Jul-26 17:00	05-May-26 08:00 A	16-Sep-26 12:00 A	0.00	0.00	0.00	0%	0%	-47
PG-Q-PR-LL-LS-MF-10	Bike and Walk Path Materials(Completed)	40	05-May-26 08:00	25-Jun-26 10:00	05-May-26 08:00 A	24-Jun-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-Q-PR-LL-LS-MF-10_R	Bike and Walk Path Materials(Remaining)	10	25-Jun-26 08:00	06-Jul-26 17:00	30-Jul-26 08:00 A	16-Sep-26 12:00 A	0.00	0.00	0.00	100%	100%	-32
PG-Q-PR-LL-LS-MF-20	Benches, Seats (Rectangular & Circular)(Completed)	40	05-May-26 08:00	25-Jun-26 10:00	05-May-26 08:00 A	24-Jun-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-Q-PR-LL-LS-MF-20_R	Benches, Seats (Rectangular & Circular)(Remaining)	25	25-Jun-26 08:00	23-Jul-26 17:00	30-Jul-26 08:00 A	16-Sep-26 12:00 A	0.00	0.00	0.00	100%	100%	-17
PG-Q-PR-LL-LS-MF-30	Fence, gates and accessories(Completed)	40	05-May-26 08:00	25-Jun-26 10:00	05-May-26 08:00 A	24-Jun-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-Q-PR-LL-LS-MF-30_R	Fence, gates and accessories(Remaining)	25	25-Jun-26 08:00	23-Jul-26 17:00	14-Aug-26 08:00 A	16-Sep-26 12:00 A	0.00	0.00	0.00	100%	100%	-4
SPORTS & RECREATIONAL FACILITIES WORK		123	05-May-26 08:00	11-Aug-26 17:00	05-May-26 08:00 A	16-Sep-26 12:00 A	0.00	0.00	0.00	0%	0%	-31
PG-Q-PR-LL-SP-MF-10	Football Playground Materials (Flooring, goal post, nets, paints,	40	05-May-26 08:00	25-Jun-26 10:00	05-May-26 08:00 A	24-Jun-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-Q-PR-LL-SP-MF-10_R	Football Playground Materials (Flooring, goal post, nets, paints,	25	25-Jun-26 08:00	23-Jul-26 17:00	30-Jul-26 08:00 A	16-Sep-26 12:00 A	0.00	0.00	0.00	100%	100%	-17
PG-Q-PR-LL-SP-MF-20	Basketball Playground Materials (Flooring, basketball poll, nets, paints,	40	05-May-26 08:00	25-Jun-26 10:00	05-May-26 08:00 A	24-Jun-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-Q-PR-LL-SP-MF-20_R	Basketball Playground Materials (Flooring, basketball poll, nets, paints,	25	25-Jun-26 08:00	23-Jul-26 17:00	14-Aug-26 08:00 A	16-Sep-26 12:00 A	0.00	0.00	0.00	100%	100%	-4
PG-Q-PR-LL-SP-MF-30	Padel Playgound Materials (Flooring, fence, tempered glass,	40	05-May-26 08:00	25-Jun-26 10:00	05-May-26 08:00 A	24-Jun-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-Q-PR-LL-SP-MF-30_R	Padel Playgound Materials (Flooring, fence, tempered glass,	15	25-Jun-26 08:00	12-Jul-26 17:00	30-Jul-26 08:00 A	16-Sep-26 12:00 A	0.00	0.00	0.00	100%	100%	-27
PG-Q-PR-LL-SP-MF-40	Tartan Floor(Completed)	40	05-May-26 08:00	25-Jun-26 10:00	05-May-26 08:00 A	24-Jun-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-Q-PR-LL-SP-MF-40_R	Tartan Floor(Remaining)	25	25-Jun-26 08:00	23-Jul-26 17:00	22-Jul-26 08:00 A	16-Sep-26 12:00 A	0.00	0.00	0.00	100%	100%	-24
PG-Q-PR-LL-SP-MF-50	Air Dome Materials	28	11-Jul-26 08:00	11-Aug-26 17:00	27-Aug-26 08:00 A	16-Sep-26 12:00 A	0.00	0.00	0.00	100%	100%	11
CONCRETE WORK		69	05-May-26 08:00	12-Jul-26 17:00	05-May-26 08:00 A	24-Jun-26 17:00 A	0.00	0.00	0.00	0%	0%	15

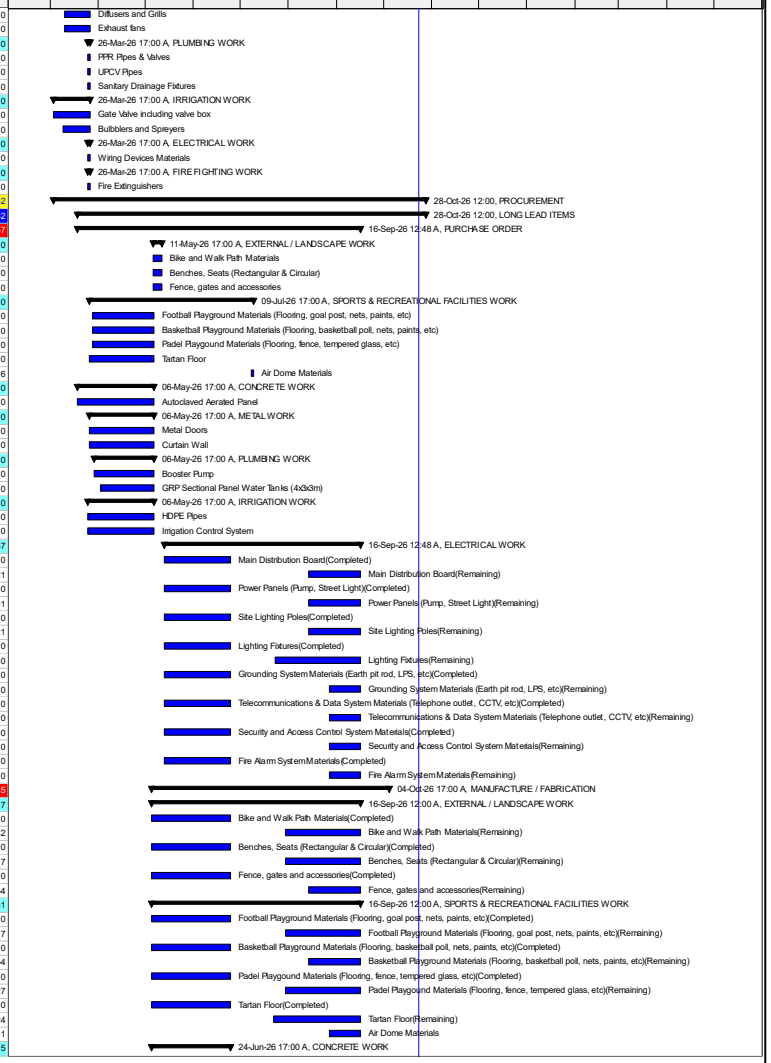


Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining W...
Milestone
summary

Baseline Schedule Rev.00

PLAYGROUNDS INITIATIVE - QASSIM, HAIL & TABUK - 25-Oct-2026

Activity ID	Activity Name	O.D	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Schedule % Complete	Performance % Complete	Variance - BL Project Duration
PG-Q-PR-LL-CO-MF-10	Autoclaved Aerated Panel(Completed)	40	05-May-26 08:00	25-Jun-26 10:00	05-May-26 08:00 A	24-Jun-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-Q-PR-LL-CO-MF-10_R	Autoclaved Aerated Panel(Remaining)	15	25-Jun-26 08:00	12-Jul-26 17:00	01-Jun-26 08:00 A	04-Jun-26 17:00 A	0.00	0.00	0.00	100%	100%	11
METAL WORK		161	05-May-26 08:00	23-Jul-26 17:00	05-May-26 08:00 A	04-Oct-26 17:00 A	0.00	0.00	0.00	0%	0%	-61
PG-Q-PR-LL-MT-MF-10	Metal Doors(Completed)	40	05-May-26 08:00	25-Jun-26 10:00	05-May-26 08:00 A	24-Jun-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-Q-PR-LL-MT-MF-10_R	Metal Doors(Remaining)	25	25-Jun-26 08:00	23-Jul-26 17:00	06-Sep-26 08:00 A	02-Oct-26 17:00 A	0.00	0.00	0.00	100%	100%	3
PG-Q-PR-LL-MT-MF-20	Curtain Wall(Completed)	40	05-May-26 08:00	25-Jun-26 10:00	05-May-26 08:00 A	24-Jun-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-Q-PR-LL-MT-MF-20_R	Curtain Wall(Remaining)	25	25-Jun-26 08:00	23-Jul-26 17:00	17-Sep-26 08:00 A	04-Oct-26 17:00 A	0.00	0.00	0.00	100%	100%	11
PLUMBING WORK		79	05-May-26 08:00	23-Jul-26 17:00	05-May-26 08:00 A	24-Jun-26 17:00 A	0.00	0.00	0.00	0%	0%	25
PG-Q-PR-LL-PB-MF-10	Booster Pump(Completed)	40	05-May-26 08:00	25-Jun-26 10:00	05-May-26 08:00 A	24-Jun-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-Q-PR-LL-PB-MF-10_R	Booster Pump(Remaining)	25	25-Jun-26 08:00	23-Jul-26 17:00	11-Jun-26 08:00 A	15-Jun-26 17:00 A	0.00	0.00	0.00	100%	100%	21
PG-Q-PR-LL-PB-MF-20	GRP Sectional Panel Water Tanks (4x3x3m)(Completed)	40	05-May-26 08:00	25-Jun-26 10:00	05-May-26 08:00 A	24-Jun-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-Q-PR-LL-PB-MF-20_R	GRP Sectional Panel Water Tanks (4x3x3m)(Remaining)	25	25-Jun-26 08:00	23-Jul-26 17:00	06-Jun-26 08:00 A	09-Jun-26 17:00 A	0.00	0.00	0.00	100%	100%	21
IRRIGATION WORK		82	05-May-26 08:00	06-Jul-26 17:00	05-May-26 08:00 A	16-Sep-26 12:00 A	0.00	0.00	0.00	0%	0%	-62
PG-Q-PR-LL-IR-MF-10	HDPE Pipes(Completed)	40	05-May-26 08:00	25-Jun-26 10:00	05-May-26 08:00 A	24-Jun-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-Q-PR-LL-IR-MF-10_R	HDPE Pipes(Remaining)	10	25-Jun-26 08:00	06-Jul-26 17:00	02-Jun-26 08:00 A	04-Jun-26 17:00 A	0.00	0.00	0.00	100%	100%	7
PG-Q-PR-LL-IR-MF-20	Irrigation Control System(Completed)	40	05-May-26 08:00	25-Jun-26 10:00	05-May-26 08:00 A	24-Jun-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-Q-PR-LL-IR-MF-20_R	Irrigation Control System(Remaining)	10	25-Jun-26 08:00	06-Jul-26 17:00	30-Jul-26 08:00 A	16-Sep-26 12:00 A	0.00	0.00	0.00	100%	100%	-32
ELECTRICAL WORK		129	12-May-26 08:00	10-Aug-26 17:00	12-May-26 08:00 A	16-Sep-26 12:00 A	0.00	0.00	0.00	0%	0%	-32
PG-Q-PR-LL-EL-MF-10	Main Distribution Board(Completed)	34	12-May-26 08:00	25-Jun-26 10:00	12-May-26 08:00 A	24-Jun-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-Q-PR-LL-EL-MF-10_R	Main Distribution Board(Remaining)	25	13-Jul-26 08:00	10-Aug-26 17:00	14-Aug-26 08:00 A	16-Sep-26 12:00 A	0.00	0.00	0.00	100%	100%	-4
PG-Q-PR-LL-EL-MF-20	Power Panels (Pump, Street Light)(Completed)	34	12-May-26 08:00	25-Jun-26 10:00	12-May-26 08:00 A	24-Jun-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-Q-PR-LL-EL-MF-20_R	Power Panels (Pump, Street Light)(Remaining)	15	13-Jul-26 08:00	29-Jul-26 17:00	14-Aug-26 08:00 A	16-Sep-26 12:00 A	0.00	0.00	0.00	100%	100%	-14
PG-Q-PR-LL-EL-MF-30	Site Lighting Poles(Completed)	34	12-May-26 08:00	25-Jun-26 10:00	12-May-26 08:00 A	24-Jun-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-Q-PR-LL-EL-MF-30_R	Site Lighting Poles(Remaining)	25	13-Jul-26 08:00	10-Aug-26 17:00	14-Aug-26 08:00 A	16-Sep-26 12:00 A	0.00	0.00	0.00	100%	100%	-4
PG-Q-PR-LL-EL-MF-40	Lighting Fixtures(Completed)	34	12-May-26 08:00	25-Jun-26 10:00	12-May-26 08:00 A	24-Jun-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-Q-PR-LL-EL-MF-40_R	Lighting Fixtures(Remaining)	25	13-Jul-26 08:00	10-Aug-26 17:00	14-Aug-26 08:00 A	16-Sep-26 12:00 A	0.00	0.00	0.00	100%	100%	-4
PG-Q-PR-LL-EL-MF-50	Grounding System Materials (Earth pit rod, LPS, etc)(Completed)	34	12-May-26 08:00	25-Jun-26 10:00	12-May-26 08:00 A	24-Jun-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-Q-PR-LL-EL-MF-50_R	Grounding System Materials (Earth pit rod, LPS, etc)(Remaining)	25	13-Jul-26 08:00	10-Aug-26 17:00	27-Aug-26 08:00 A	16-Sep-26 12:00 A	0.00	0.00	0.00	100%	100%	8
PG-Q-PR-LL-EL-MF-60	Telecommunications & Data System Materials (Telephone outlet, CCTV,	34	12-May-26 08:00	25-Jun-26 10:00	12-May-26 08:00 A	24-Jun-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-Q-PR-LL-EL-MF-60_R	Telecommunications & Data System Materials (Telephone outlet, CCTV,	25	13-Jul-26 08:00	10-Aug-26 17:00	27-Aug-26 08:00 A	16-Sep-26 12:00 A	0.00	0.00	0.00	100%	100%	8
PG-Q-PR-LL-EL-MF-70	Security and Access Control System Materials(Completed)	34	12-May-26 08:00	25-Jun-26 10:00	12-May-26 08:00 A	24-Jun-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-Q-PR-LL-EL-MF-70_R	Security and Access Control System Materials(Remaining)	25	13-Jul-26 08:00	10-Aug-26 17:00	27-Aug-26 08:00 A	16-Sep-26 12:00 A	0.00	0.00	0.00	100%	100%	8
PG-Q-PR-LL-EL-MF-80	Fire Alarm System Materials(Completed)	34	12-May-26 08:00	25-Jun-26 10:00	12-May-26 08:00 A	24-Jun-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-Q-PR-LL-EL-MF-80_R	Fire Alarm System Materials(Remaining)	25	13-Jul-26 08:00	10-Aug-26 17:00	27-Aug-26 08:00 A	16-Sep-26 12:00 A	0.00	0.00	0.00	100%	100%	8
DELIVERY TO SITE		175	06-May-26 08:00	27-Aug-26 17:00	06-May-26 08:00 A	28-Oct-26 12:00	3,229,967.34	2,816,604.28	3,229,967.34	100%	87.2%	-52
EXTERNAL / LANDSCAPE WORK		123	06-May-26 08:00	10-Aug-26 17:00	06-May-26 08:00 A	25-Oct-26 12:00	178,309.62	176,866.75	178,309.62	100%	99.19%	-64
PG-Q-PR-LL-LS-DL-10	Bike and Walk Path Materials(Completed)	39	06-May-26 08:00	24-Jun-26 17:00	06-May-26 08:00 A	24-Jun-26 17:00 A	71,685.00	71,685.00	71,685.00	100%	100%	0
PG-Q-PR-LL-LS-DL-10_R	Bike and Walk Path Materials(Remaining)	9	07-Jul-26 08:00	16-Jul-26 17:00	14-Aug-26 08:00 A	26-Sep-26 16:12 A	47,790.00	47,790.00	47,790.00	100%	100%	-27
PG-Q-PR-LL-LS-DL-20	Benches, Seats (Rectangular & Circular)(Completed)	39	06-May-26 08:00	24-Jun-26 17:00	06-May-26 08:00 A	24-Jun-26 17:00 A	21,643.04	21,643.04	21,643.04	100%	100%	0
PG-Q-PR-LL-LS-DL-20_R	Benches, Seats (Rectangular & Circular)(Remaining)	15	25-Jul-26 08:00	10-Aug-26 17:00	14-Aug-26 08:00 A	25-Oct-26 12:00	14,428.69	12,985.82	14,428.69	100%	90%	-46
PG-Q-PR-LL-LS-DL-30	Fence, gates and accessories(Completed)	39	06-May-26 08:00	24-Jun-26 17:00	06-May-26 08:00 A	24-Jun-26 17:00 A	11,381.45	11,381.45	11,381.45	100%	100%	0
PG-Q-PR-LL-LS-DL-30_R	Fence, gates and accessories(Remaining)	15	25-Jul-26 08:00	10-Aug-26 17:00	14-Aug-26 08:00 A	30-Sep-26 12:00 A	11,381.45	11,381.45	11,381.45	100%	100%	-25
SPORTS & RECREATIONAL FACILITIES WORK		127	06-May-26 08:00	23-Aug-26 17:00	06-May-26 08:00 A	27-Oct-26 15:24	2,461,702.86	2,073,940.31	2,461,702.86	100%	84.25%	-55
PG-Q-PR-LL-SPDL-10	Football Playground Materials (Flooring, goal post, nets, paints,	39	06-May-26 08:00	24-Jun-26 17:00	06-May-26 08:00 A	24-Jun-26 17:00 A	70,478.10	70,478.10	70,478.10	100%	100%	0
PG-Q-PR-LL-SPDL-10_R	Football Playground Materials (Flooring, goal post, nets, paints,	15	25-Jul-26 08:00	10-Aug-26 17:00	14-Aug-26 08:00 A	24-Oct-26 15:00	46,985.40	44,636.13	46,985.40	100%	95%	-45
PG-Q-PR-LL-SPDL-20	Basketball Playground Materials (Flooring, basketball poll, nets, paints,	39	06-May-26 08:00	24-Jun-26 17:00	06-May-26 08:00 A	24-Jun-26 17:00 A	10,152.00	10,152.00	10,152.00	100%	100%	0
PG-Q-PR-LL-SPDL-20_R	Basketball Playground Materials (Flooring, basketball poll, nets, paints,	15	25-Jul-26 08:00	10-Aug-26 17:00	14-Aug-26 08:00 A	24-Oct-26 15:00	10,152.00	9,644.40	10,152.00	100%	95%	-45
PG-Q-PR-LL-SPDL-30	Padel Playgound Materials (Fence, tempered glass, etc)(Completed)	39	06-May-26 08:00	24-Jun-26 17:00	06-May-26 08:00 A	24-Jun-26 17:00 A	26,778.60	26,778.60	26,778.60	100%	100%	0
PG-Q-PR-LL-SPDL-30_R	Padel Playgound Materials (Fence, tempered glass, etc)(Remaining)	15	13-Jul-26 08:00	29-Jul-26 17:00	14-Aug-26 08:00 A	24-Oct-26 15:00	26,778.60	25,439.67	26,778.60	100%	95%	-45
PG-Q-PR-LL-SPDL-40	Tartan Floor(Completed)	39	06-May-26 08:00	24-Jun-26 17:00	06-May-26 08:00 A	24-Jun-26 17:00 A	235,029.60	235,029.60	235,029.60	100%	100%	0
PG-Q-PR-LL-SPDL-40_R	Tartan Floor(Remaining)	15	25-Jul-26 08:00	10-Aug-26 17:00	14-Aug-26 08:00 A	24-Oct-26 15:00	156,686.40	148,852.08	156,686.40	100%	95%	-45
PG-Q-PR-LL-SPDL-50	Air Dome Materials	10	12-Aug-26 08:00	23-Aug-26 17:00	24-Oct-26 08:00 A	27-Oct-26 15:24	1,878,662.16	1,502,929.73	1,878,662.16	100%	80%	6
CONCRETE WORK		78	06-May-26 08:00	23-Jul-26 17:00	06-May-26 08:00 A	05-Jul-26 17:00 A	12,757.50	12,757.50	12,757.50	100%	100%	16
PG-Q-PR-LL-CO-DL-10	Autoclaved Aerated Panel(Completed)	39	06-May-26 08:00	24-Jun-26 17:00	06-May-26 08:00 A	24-Jun-26 17:00 A	7,654.50	7,654.50	7,654.50	100%	100%	0
PG-Q-PR-LL-CO-DL-10_R	Autoclaved Aerated Panel(Remaining)	10	13-Jul-26 08:00	23-Jul-26 17:00	04-Jul-26 08:00 A	05-Jul-26 17:00 A	5,103.00	5,103.00	5,103.00	100%	100%	8
METAL WORK		175	06-May-26 08:00	10-Aug-26 17:00	06-May-26 08:00 A	28-Oct-26 12:00	8,003.07	6,974.78	8,003.07	100%	87.15%	-67
PG-Q-PR-LL-MT-DL-10	Metal Doors(Completed)	39	06-May-26 08:00	24-Jun-26 17:00	06-May-26 08:00 A	24-Jun-26 17:00 A	573.89	573.89	573.89	100%	100%	0
PG-Q-PR-LL-MT-DL-10_R	Metal Doors(Remaining)	15	25-Jul-26 08:00	10-Aug-26 17:00	27-Aug-26 08:00 A	02-Oct-26 12:00 A	573.89	573.89	573.89	100%	100%	-15
PG-Q-PR-LL-MT-DL-20	Curtain Wall(Completed)	39	06-May-26 08:00	24-Jun-26 17:00	06-May-26 08:00 A	24-Jun-26 17:00 A	3,427.65	3,427.65	3,427.65	100%	100%	0
PG-Q-PR-LL-MT-DL-20_R	Curtain Wall(Remaining)	15	25-Jul-26 08:00	10-Aug-26 17:00	05-Oct-26 08:00 A	28-Oct-26 12:00	3,427.65	2,399.36	3,427.65	100%	70%	-6
PLUMBING WORK		104	06-May-26 08:00	10-Aug-26 17:00	06-May-26 08:00 A	13-Oct-26 17:00 A	31,985.55	31,985.55	31,985.55	100%	100%	-54
PG-Q-PR-LL-PB-DL-10	Booster Pump(Completed)	39	06-May-26 08:00	24-Jun-26 17:00	06-May-26 08:00 A	24-Jun-26 17:00 A	8,182.35	8,182.35	8,182.35	100%	100%	0
PG-Q-PR-LL-PB-DL-10_R	Booster Pump(Remaining)	15	25-Jul-26 08:00	10-Aug-26 17:00	20-Aug-26 08:00 A	30-Sep-26 12:00 A	8,182.35	8,182.35	8,182.35	100%	100%	-20
PG-Q-PR-LL-PB-DL-20	GRP Sectional Panel Water Tanks (4x3x3m)(Completed)	39	06-May-26 08:00	24-Jun-26 17:00	06-May-26 08:00 A	24-Jun-26 17:00 A	7,810.43	7,810.43	7,810.43	100%	100%	0
PG-Q-PR-LL-PB-DL-20_R	GRP Sectional Panel Water Tanks (4x3x3m)(Remaining)	15	25-Jul-26 08:00	10-Aug-26 17:00	14-Aug-26 08:00 A	13-Oct-26 17:00 A	7,810.43	7,810.43	7,810.43	100%	100%	-36
IRRIGATION WORK		102	06-May-26 08:00	15-Jul-26 17:00	06-May-26 08:00 A	24-Oct-26 11:12	220,380.75	219,357.96	220,380.75	100%	99.54%	-84
PG-Q-PR-LL-IR-DL-10	HDPE Pipes(Completed)	39	06-May-26 08:00	24-Jun-26 17:00	06-May-26 08:00 A	24-Jun-26 17:00 A	89,734.50	89,734.50	89,734.50	100%	100%	0
PG-Q-PR-LL-IR-DL-10_R	HDPE Pipes(Remaining)	7	07-Jul-26 08:00	14-Jul-26 17:00	14-Aug-26 08:00 A	27-Aug-26 17:00 A	89,734.50	89,734.50	89,734.50	100%	100%	-5
PG-Q-PR-LL-IR-DL-20	Irrigation Control System(Completed)	39	06-May-26 08:00	24-Jun-26 17:00	06-May-26 08:00 A	24-Jun-26 17:00 A	20,455.88	20,455.88	20,455.88	100%	100%	0
PG-Q-PR-LL-IR-DL-20_R	Irrigation Control System(Remaining)	8	07-Jul-26 08:00	15-Jul-26 17:00	20-Aug-26 08:00 A	24-Oct-26 11:12	20,455.88	19,433.08	20,455.88	100%	95%	-46
ELECTRICAL WORK		143	13-May-26 08:00	27-Aug-26 17:00	13-May-26 08:00 A	25-Oct-26 12:00	316,827.99	294,721.44	316,827.99	100%	93.02%	-49
PG-Q-PR-LL-EL-DL-10	Main Distribution Board(Completed)	33	13-May-26 08:00	24-Jun-26 17:00	13-May-26 08:00 A	24-Jun-26 17:00 A	1,338.93	1,338.93	1,338.93	100%	100%	0
PG-Q-PR-LL-EL-DL-10_R	Main Distribution Board(Remaining)	15	11-Aug-26 08:00	27-Aug-26 17:00	14-Aug-26 08:00 A	25-Oct-26 12:00	3,124.17	2,811.75	3,124.17	100%	90%	-46

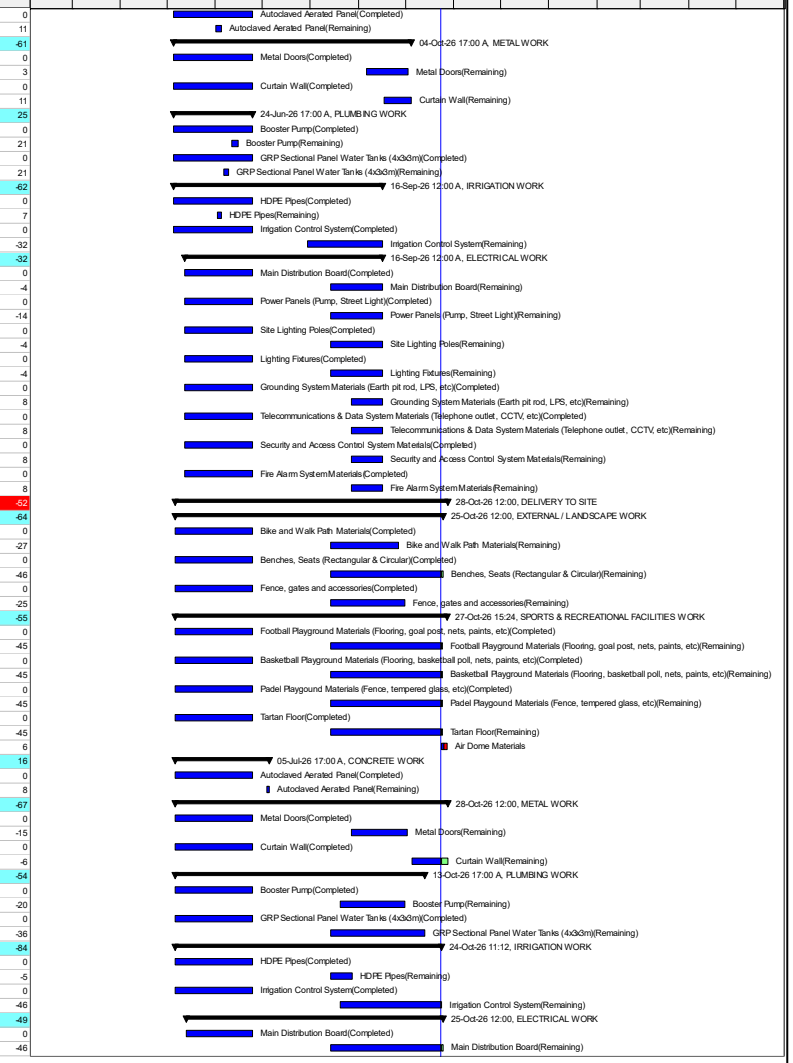


Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining W...
Milestone
summary

Baseline Schedule Rev.00

PLAYGROUNDS INITIATIVE - QASSIM, HAIL & TABUK - 25-Oct-2026

Activity ID	Activity Name	O.D	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Schedule % Complete	Performance % Complete	Variance - BL Project Duration
PG-Q-PR-LL-EL-DL-20	Power Panels (Pump, Street Light)(Completed)	33	13-May-26 08:00	24-Jun-26 17:00	13-May-26 08:00 A	24-Jun-26 17:00 A	1,785.24	1,785.24	1,785.24	100%	100%	0
PG-Q-PR-LL-EL-DL-20_R	Power Panels (Pump, Street Light)(Remaining)	10	30-Jul-26 08:00	10-Aug-26 17:00	14-Aug-26 08:00 A	24-Oct-26 17:00	1,785.24	1,606.72	1,785.24	100%	90%	-50
PG-Q-PR-LL-EL-DL-30	Site Lighting Poles(Completed)	33	13-May-26 08:00	24-Jun-26 17:00	13-May-26 08:00 A	24-Jun-26 17:00 A	78,323.76	78,323.76	78,323.76	100%	100%	0
PG-Q-PR-LL-EL-DL-30_R	Site Lighting Poles(Remaining)	15	11-Aug-26 08:00	27-Aug-26 17:00	14-Aug-26 08:00 A	25-Oct-26 12:00	182,755.44	164,479.90	182,755.44	100%	90%	-46
PG-Q-PR-LL-EL-DL-40	Lighting Fixtures(Completed)	33	13-May-26 08:00	24-Jun-26 17:00	13-May-26 08:00 A	24-Jun-26 17:00 A	3,463.64	3,463.64	3,463.64	100%	100%	0
PG-Q-PR-LL-EL-DL-40_R	Lighting Fixtures(Remaining)	15	11-Aug-26 08:00	27-Aug-26 17:00	14-Aug-26 08:00 A	25-Oct-26 12:00	8,081.83	7,273.65	8,081.83	100%	90%	-46
PG-Q-PR-LL-EL-DL-50	Grounding System Materials (Earth pit rod, LPS, etc)(Completed)	33	13-May-26 08:00	24-Jun-26 17:00	13-May-26 08:00 A	24-Jun-26 17:00 A	2,711.31	2,711.31	2,711.31	100%	100%	0
PG-Q-PR-LL-EL-DL-50_R	Grounding System Materials (Earth pit rod, LPS, etc)(Remaining)	15	11-Aug-26 08:00	27-Aug-26 17:00	27-Aug-26 08:00 A	25-Oct-26 12:00	6,326.40	5,693.76	6,326.40	100%	90%	-35
PG-Q-PR-LL-EL-DL-60	Telecommunications & Data System Materials (Telephone outlet, CCTV,	33	13-May-26 08:00	24-Jun-26 17:00	13-May-26 08:00 A	24-Jun-26 17:00 A	2,644.33	2,644.33	2,644.33	100%	100%	0
PG-Q-PR-LL-EL-DL-60_R	Telecommunications & Data System Materials (Telephone outlet, CCTV,	15	11-Aug-26 08:00	27-Aug-26 17:00	27-Aug-26 08:00 A	25-Oct-26 12:00	6,170.09	5,553.08	6,170.09	100%	90%	-35
PG-Q-PR-LL-EL-DL-70	Security and Access Control System Materials(Completed)	33	13-May-26 08:00	24-Jun-26 17:00	13-May-26 08:00 A	24-Jun-26 17:00 A	3,347.73	3,347.73	3,347.73	100%	100%	0
PG-Q-PR-LL-EL-DL-70_R	Security and Access Control System Materials(Remaining)	15	11-Aug-26 08:00	27-Aug-26 17:00	27-Aug-26 08:00 A	25-Oct-26 12:00	7,811.37	7,030.23	7,811.37	100%	90%	-35
PG-Q-PR-LL-EL-DL-80	Fire Alarm System Materials(Completed)	33	13-May-26 08:00	24-Jun-26 17:00	13-May-26 08:00 A	24-Jun-26 17:00 A	2,147.55	2,147.55	2,147.55	100%	100%	0
PG-Q-PR-LL-EL-DL-80_R	Fire Alarm System Materials(Remaining)	15	11-Aug-26 08:00	27-Aug-26 17:00	27-Aug-26 08:00 A	25-Oct-26 12:00	5,010.96	4,509.86	5,010.96	100%	90%	-35
SHORT LEAD ITEMS		183	03-Mar-26 08:00	12-Jul-26 17:00	03-Mar-26 08:00 A	25-Oct-26 12:00	1,505,168.46	1,489,796.57	1,505,168.46	100%	98.98%	-89
PURCHASE ORDER		64	03-Mar-26 08:00	21-May-26 10:00	03-Mar-26 08:00 A	20-May-26 17:00 A	0.00	0.00	0.00	0%	0%	0
EXTERNAL / LANDSCAPE WORK		57	03-Mar-26 08:00	13-May-26 10:00	03-Mar-26 08:00 A	12-May-26 17:00 A	0.00	0.00	0.00	0%	0%	0
PG-Q-PR-SL-LS-PO-10	Backfilling Materials	40	03-Mar-26 08:00	23-Apr-26 10:00	03-Mar-26 08:00 A	22-Apr-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-Q-PR-SL-LS-PO-20	Interlock tiles	25	01-Apr-26 08:00	30-Apr-26 10:00	01-Apr-26 08:00 A	29-Apr-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-Q-PR-SL-LS-PO-30	Compacted Natural Ground Soil	37	07-Mar-26 08:00	23-Apr-26 10:00	07-Mar-26 08:00 A	22-Apr-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-Q-PR-SL-LS-PO-40	Curb Stone	28	29-Mar-26 08:00	30-Apr-26 10:00	29-Mar-26 08:00 A	29-Apr-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-Q-PR-SL-LS-PO-50	Thermoplastic pavement road marking	2	11-May-26 08:00	13-May-26 10:00	11-May-26 08:00 A	12-May-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-Q-PR-SL-LS-PO-60	Traffic Signages	2	11-May-26 08:00	13-May-26 10:00	11-May-26 08:00 A	12-May-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-Q-PR-SL-LS-PO-70	Trees	2	11-May-26 08:00	13-May-26 10:00	11-May-26 08:00 A	12-May-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-Q-PR-SL-LS-PO-80	Lawn	2	11-May-26 08:00	13-May-26 10:00	11-May-26 08:00 A	12-May-26 17:00 A	0.00	0.00	0.00	100%	100%	0
CONCRETE WORK		39	04-Mar-26 08:00	23-Apr-26 10:00	04-Mar-26 08:00 A	22-Apr-26 17:00 A	0.00	0.00	0.00	0%	0%	0
PG-Q-PR-SL-CO-PO-10	Steel Rebar	39	04-Mar-26 08:00	23-Apr-26 10:00	04-Mar-26 08:00 A	22-Apr-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-Q-PR-SL-CO-PO-20	Concrete	34	10-Mar-26 08:00	23-Apr-26 10:00	10-Mar-26 08:00 A	22-Apr-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-Q-PR-SL-CO-PO-30	Screed	19	01-Apr-26 08:00	23-Apr-26 10:00	01-Apr-26 08:00 A	22-Apr-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-Q-PR-SL-CO-PO-40	CMU Block	30	15-Mar-26 08:00	23-Apr-26 10:00	15-Mar-26 08:00 A	22-Apr-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-Q-PR-SL-CO-PO-50	Concrete Repair & Protection Materials	30	15-Mar-26 08:00	23-Apr-26 10:00	15-Mar-26 08:00 A	22-Apr-26 17:00 A	0.00	0.00	0.00	100%	100%	0
ARCHITECTURAL & FINISHES WORK		48	07-Mar-26 08:00	06-May-26 10:00	07-Mar-26 08:00 A	05-May-26 17:00 A	0.00	0.00	0.00	0%	0%	0
PG-Q-PR-SL-AR-PO-10	Ceramic tiles	32	30-Mar-26 08:00	06-May-26 10:00	30-Mar-26 08:00 A	05-May-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-Q-PR-SL-AR-PO-100	Gypsum Boards	32	30-Mar-26 08:00	06-May-26 10:00	30-Mar-26 08:00 A	05-May-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-Q-PR-SL-AR-PO-110	Specialities Materials (Toilet accessories, lockers, logo, etc)	32	30-Mar-26 08:00	06-May-26 10:00	30-Mar-26 08:00 A	05-May-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-Q-PR-SL-AR-PO-120	Waterproofing System Materials	32	30-Mar-26 08:00	06-May-26 10:00	30-Mar-26 08:00 A	05-May-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-Q-PR-SL-AR-PO-20	Anti-slip Granite tiles	32	30-Mar-26 08:00	06-May-26 10:00	30-Mar-26 08:00 A	05-May-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-Q-PR-SL-AR-PO-30	Epoxy Paint	32	30-Mar-26 08:00	06-May-26 10:00	30-Mar-26 08:00 A	05-May-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-Q-PR-SL-AR-PO-40	Cement Plaster	48	07-Mar-26 08:00	06-May-26 10:00	07-Mar-26 08:00 A	05-May-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-Q-PR-SL-AR-PO-50	Acrylic Paint	45	10-Mar-26 08:00	06-May-26 10:00	10-Mar-26 08:00 A	05-May-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-Q-PR-SL-AR-PO-60	Stone Cladding	30	01-Apr-26 08:00	06-May-26 10:00	01-Apr-26 08:00 A	05-May-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-Q-PR-SL-AR-PO-70	Aluminum Plates	30	01-Apr-26 08:00	06-May-26 10:00	01-Apr-26 08:00 A	05-May-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-Q-PR-SL-AR-PO-80	Phenolic Partition	40	16-Mar-26 08:00	06-May-26 10:00	16-Mar-26 08:00 A	05-May-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-Q-PR-SL-AR-PO-90	Glass Partition	40	16-Mar-26 08:00	06-May-26 10:00	16-Mar-26 08:00 A	05-May-26 17:00 A	0.00	0.00	0.00	100%	100%	0
METAL WORK		36	25-Mar-26 08:00	06-May-26 10:00	25-Mar-26 08:00 A	05-May-26 17:00 A	0.00	0.00	0.00	0%	0%	0
PG-Q-PR-SL-MT-PO-10	Galvanized Steel Ladder	36	25-Mar-26 08:00	06-May-26 10:00	25-Mar-26 08:00 A	05-May-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-Q-PR-SL-MT-PO-20	Galvanized Steel Roof Scupper	2	04-May-26 08:00	06-May-26 10:00	04-May-26 08:00 A	05-May-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-Q-PR-SL-MT-PO-30	Galvanized Steel Cover with frame	2	04-May-26 08:00	06-May-26 10:00	04-May-26 08:00 A	05-May-26 17:00 A	0.00	0.00	0.00	100%	100%	0
HVAC WORK		46	09-Mar-26 08:00	06-May-26 10:00	09-Mar-26 08:00 A	05-May-26 17:00 A	0.00	0.00	0.00	0%	0%	0
PG-Q-PR-SL-AC-PO-10	Split Air Conditioning Unit	46	09-Mar-26 08:00	06-May-26 10:00	09-Mar-26 08:00 A	05-May-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-Q-PR-SL-AC-PO-20	Air Duct	42	14-Mar-26 08:00	06-May-26 10:00	14-Mar-26 08:00 A	05-May-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-Q-PR-SL-AC-PO-30	Diffusers and Grills	34	28-Mar-26 08:00	06-May-26 10:00	28-Mar-26 08:00 A	05-May-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-Q-PR-SL-AC-PO-40	Exhaust fans	27	05-Apr-26 08:00	06-May-26 10:00	05-Apr-26 08:00 A	05-May-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PLUMBING WORK		33	29-Mar-26 08:00	06-May-26 10:00	29-Mar-26 08:00 A	05-May-26 17:00 A	0.00	0.00	0.00	0%	0%	0
PG-Q-PR-SL-PB-PO-10	PPR Pipes & Valves	33	29-Mar-26 08:00	06-May-26 10:00	29-Mar-26 08:00 A	05-May-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-Q-PR-SL-PB-PO-20	UPCV Pipes	33	29-Mar-26 08:00	06-May-26 10:00	29-Mar-26 08:00 A	05-May-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-Q-PR-SL-PB-PO-30	Sanitary Drainage Fixtures	33	29-Mar-26 08:00	06-May-26 10:00	29-Mar-26 08:00 A	05-May-26 17:00 A	0.00	0.00	0.00	100%	100%	0
IRRIGATION WORK		43	12-Mar-26 08:00	06-May-26 10:00	12-Mar-26 08:00 A	05-May-26 17:00 A	0.00	0.00	0.00	0%	0%	0
PG-Q-PR-SL-IR-PO-10	Gate Valve including valve box	43	12-Mar-26 08:00	06-May-26 10:00	12-Mar-26 08:00 A	05-May-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-Q-PR-SL-IR-PO-20	Bubblers and Sprayers	38	18-Mar-26 08:00	06-May-26 10:00	18-Mar-26 08:00 A	05-May-26 17:00 A	0.00	0.00	0.00	100%	100%	0
ELECTRICAL WORK		8	12-May-26 08:00	21-May-26 10:00	12-May-26 08:00 A	20-May-26 17:00 A	0.00	0.00	0.00	0%	0%	0
PG-Q-PR-SL-EL-PO-10	Wiring Devices Materials	8	12-May-26 08:00	21-May-26 10:00	12-May-26 08:00 A	20-May-26 17:00 A	0.00	0.00	0.00	100%	100%	0
FIRE FIGHTING WORK		30	01-Apr-26 08:00	06-May-26 10:00	01-Apr-26 08:00 A	05-May-26 17:00 A	0.00	0.00	0.00	0%	0%	0
PG-Q-PR-SL-FF-PO-10	Fire Extinguishers	30	01-Apr-26 08:00	06-May-26 10:00	01-Apr-26 08:00 A	05-May-26 17:00 A	0.00	0.00	0.00	100%	100%	0
DELIVERY TO SITE		181	05-Mar-26 08:00	12-Jul-26 17:00	05-Mar-26 08:00 A	25-Oct-26 12:00	1,505,168.46	1,489,796.57	1,505,168.46	100%	98.98%	-89
EXTERNAL / LANDSCAPE WORK		155	05-Mar-26 08:00	08-Jul-26 17:00	05-Mar-26 08:00 A	25-Oct-26 09:36	1,258,805.61	1,250,950.31	1,258,805.61	100%	99.38%	-91
PG-Q-PR-SL-LS-DL-10	Backfilling Materials	39	05-Mar-26 08:00	23-Apr-26 17:00	05-Mar-26 08:00 A	24-Apr-26 17:00 A	328,050.00	328,050.00	328,050.00	100%	100%	0
PG-Q-PR-SL-LS-DL-20	Interlock tiles	12	30-Apr-26 08:00	13-May-26 17:00	30-Apr-26 08:00 A	13-May-26 17:00 A	268,488.00	268,488.00	268,488.00	100%	100%	0
PG-Q-PR-SL-LS-DL-30	Compacted Natural Ground Soil	12	30-Apr-26 08:00	13-May-26 17:00	30-Apr-26 08:00 A	13-May-26 17:00 A	77,220.00	77,220.00	77,220.00	100%	100%	0
PG-Q-PR-SL-LS-DL-40	Curb Stone	12	30-Apr-26 08:00	13-May-26 17:00	30-Apr-26 08:00 A	13-May-26 17:00 A	388,665.00	388,665.00	388,665.00	100%	100%	0
PG-Q-PR-SL-LS-DL-50	Thermoplastic pavement road marking(Completed)	39	06-May-26 08:00	24-Jun-26 17:00	06-May-26 08:00 A	24-Jun-26 17:00 A	2,838.40	2,838.40	2,838.40	100%	100%	0
PG-Q-PR-SL-LS-DL-50_R	Thermoplastic pavement road marking(Remaining)	12	25-Jun-26 08:00	08-Jul-26 17:00	27-Aug-26 08:00 A	25-Oct-26 09:36	1,892.27	1,703.04	1,892.27	100%	90%	-37
PG-Q-PR-SL-LS-DL-60	Traffic Signages(Completed)	39	06-May-26 08:00	24-Jun-26 17:00	06-May-26 08:00 A	24-Jun-26 17:00 A	1,071.14	1,071.14	1,071.14	100%	100%	0

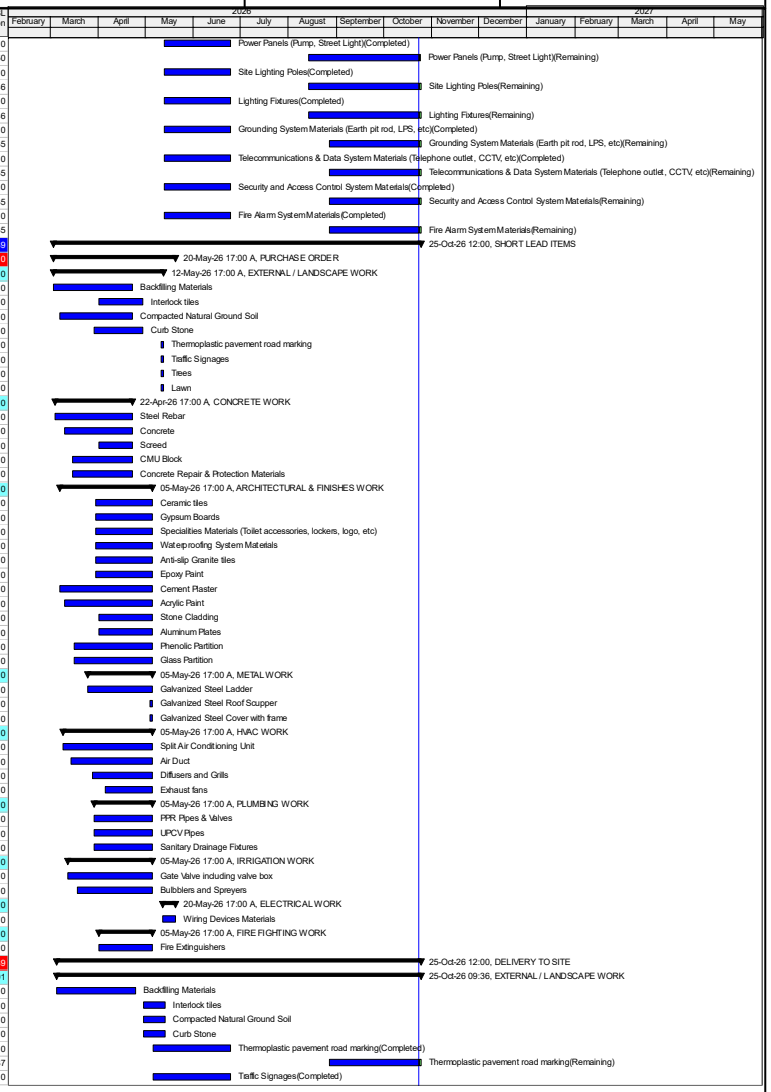


Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining W...
Milestone
summary

Baseline Schedule Rev.00

PLAYGROUNDS INITIATIVE - QASSIM, HAIL & TABUK - 25-Oct-2026

Activity ID	Activity Name	O.D	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Schedule % Complete	Performance % Complete	Variance - BL Project Duration
PG-Q-PR-SL-LS-DL-60_R	Traffic Signages(Remaining)	12	25-Jun-26 08:00	08-Jul-26 17:00	27-Aug-26 08:00 A	25-Oct-26 09:36	714.10	642.69	714.10	100%	90%	-37
PG-Q-PR-SL-LS-DL-70	Trees(Completed)	39	06-May-26 08:00	24-Jun-26 17:00	06-May-26 08:00 A	24-Jun-26 17:00 A	51,550.02	51,550.02	51,550.02	100%	100%	0
PG-Q-PR-SL-LS-DL-70_R	Trees(Remaining)	12	25-Jun-26 08:00	08-Jul-26 17:00	27-Aug-26 08:00 A	25-Oct-26 09:36	34,366.68	30,930.01	34,366.68	100%	90%	-37
PG-Q-PR-SL-LS-DL-80	Lawn(Completed)	39	06-May-26 08:00	24-Jun-26 17:00	06-May-26 08:00 A	24-Jun-26 17:00 A	62,370.00	62,370.00	62,370.00	100%	100%	0
PG-Q-PR-SL-LS-DL-80_R	Lawn(Remaining)	12	25-Jun-26 08:00	08-Jul-26 17:00	27-Aug-26 08:00 A	25-Oct-26 09:36	41,580.00	37,422.00	41,580.00	100%	90%	-37
CONCRETE WORK		50	12-Mar-26 08:00	13-May-26 17:00	12-Mar-26 08:00 A	13-May-26 17:00 A	14,485.23	14,485.23	14,485.23	100%	100%	0
PG-Q-PR-SL-CO-DL-10	Steel Rebar	18	23-Apr-26 08:00	13-May-26 17:00	23-Apr-26 08:00 A	13-May-26 17:00 A	4,291.38	4,291.38	4,291.38	100%	100%	0
PG-Q-PR-SL-CO-DL-20	Concrete	50	12-Mar-26 08:00	13-May-26 17:00	12-Mar-26 08:00 A	13-May-26 17:00 A	4,669.65	4,669.65	4,669.65	100%	100%	0
PG-Q-PR-SL-CO-DL-30	Screed	18	23-Apr-26 08:00	13-May-26 17:00	23-Apr-26 08:00 A	13-May-26 17:00 A	1,058.40	1,058.40	1,058.40	100%	100%	0
PG-Q-PR-SL-CO-DL-40	CMU Block	18	23-Apr-26 08:00	13-May-26 17:00	23-Apr-26 08:00 A	13-May-26 17:00 A	1,117.80	1,117.80	1,117.80	100%	100%	0
PG-Q-PR-SL-CO-DL-50	Concrete Repair & Protection Materials	18	23-Apr-26 08:00	13-May-26 17:00	23-Apr-26 08:00 A	13-May-26 17:00 A	3,348.00	3,348.00	3,348.00	100%	100%	0
ARCHITECTURAL & FINISHES WORK		7	06-May-26 08:00	13-May-26 17:00	06-May-26 08:00 A	13-May-26 17:00 A	71,383.95	71,383.95	71,383.95	100%	100%	0
PG-Q-PR-SL-AR-DL-10	Ceramic tiles	7	06-May-26 08:00	13-May-26 17:00	06-May-26 08:00 A	13-May-26 17:00 A	5,147.55	5,147.55	5,147.55	100%	100%	0
PG-Q-PR-SL-AR-DL-100	Gypsum Boards	7	06-May-26 08:00	13-May-26 17:00	06-May-26 08:00 A	13-May-26 17:00 A	1,697.22	1,697.22	1,697.22	100%	100%	0
PG-Q-PR-SL-AR-DL-110	Specialities Materials (Toilet accessories, lockers, logo, etc)	7	06-May-26 08:00	13-May-26 17:00	06-May-26 08:00 A	13-May-26 17:00 A	20,365.83	20,365.83	20,365.83	100%	100%	0
PG-Q-PR-SL-AR-DL-120	Waterproofing System Materials	7	06-May-26 08:00	13-May-26 17:00	06-May-26 08:00 A	13-May-26 17:00 A	4,897.80	4,897.80	4,897.80	100%	100%	0
PG-Q-PR-SL-AR-DL-20	Anti-slip Granite tiles	7	06-May-26 08:00	13-May-26 17:00	06-May-26 08:00 A	13-May-26 17:00 A	4,819.50	4,819.50	4,819.50	100%	100%	0
PG-Q-PR-SL-AR-DL-30	Epoxy Paint	7	06-May-26 08:00	13-May-26 17:00	06-May-26 08:00 A	13-May-26 17:00 A	1,000.62	1,000.62	1,000.62	100%	100%	0
PG-Q-PR-SL-AR-DL-40	Cement Plaster	7	06-May-26 08:00	13-May-26 17:00	06-May-26 08:00 A	13-May-26 17:00 A	1,992.33	1,992.33	1,992.33	100%	100%	0
PG-Q-PR-SL-AR-DL-50	Acrylic Paint	7	06-May-26 08:00	13-May-26 17:00	06-May-26 08:00 A	13-May-26 17:00 A	1,331.10	1,331.10	1,331.10	100%	100%	0
PG-Q-PR-SL-AR-DL-60	Stone Cladding	7	06-May-26 08:00	13-May-26 17:00	06-May-26 08:00 A	13-May-26 17:00 A	16,669.80	16,669.80	16,669.80	100%	100%	0
PG-Q-PR-SL-AR-DL-70	Aluminum Plates	7	06-May-26 08:00	13-May-26 17:00	06-May-26 08:00 A	13-May-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-Q-PR-SL-AR-DL-80	Phenolic Partition	7	06-May-26 08:00	13-May-26 17:00	06-May-26 08:00 A	13-May-26 17:00 A	12,063.60	12,063.60	12,063.60	100%	100%	0
PG-Q-PR-SL-AR-DL-90	Glass Partition	7	06-May-26 08:00	13-May-26 17:00	06-May-26 08:00 A	13-May-26 17:00 A	1,398.60	1,398.60	1,398.60	100%	100%	0
METAL WORK		129	06-May-26 08:00	08-Jul-26 17:00	06-May-26 08:00 A	25-Oct-26 09:36	4,310.01	4,137.61	4,310.01	100%	96%	-91
PG-Q-PR-SL-MT-DL-10	Galvanized Steel Ladder(Completed)	39	06-May-26 08:00	24-Jun-26 17:00	06-May-26 08:00 A	24-Jun-26 17:00 A	1,954.04	1,954.04	1,954.04	100%	100%	0
PG-Q-PR-SL-MT-DL-10_R	Galvanized Steel Ladder(Remaining)	12	25-Jun-26 08:00	08-Jul-26 17:00	26-Sep-26 08:00 A	25-Oct-26 09:36	1,302.70	1,172.43	1,302.70	100%	90%	-13
PG-Q-PR-SL-MT-DL-20	Galvanized Steel Roof Scupper(Completed)	39	06-May-26 08:00	24-Jun-26 17:00	06-May-26 08:00 A	24-Jun-26 17:00 A	169.13	169.13	169.13	100%	100%	0
PG-Q-PR-SL-MT-DL-20_R	Galvanized Steel Roof Scupper(Remaining)	12	25-Jun-26 08:00	08-Jul-26 17:00	26-Sep-26 08:00 A	25-Oct-26 09:36	112.75	101.48	112.75	100%	90%	-13
PG-Q-PR-SL-MT-DL-30	Galvanized Steel Cover with frame(Completed)	39	06-May-26 08:00	24-Jun-26 17:00	06-May-26 08:00 A	24-Jun-26 17:00 A	462.83	462.83	462.83	100%	100%	0
PG-Q-PR-SL-MT-DL-30_R	Galvanized Steel Cover with frame(Remaining)	12	25-Jun-26 08:00	08-Jul-26 17:00	26-Sep-26 08:00 A	25-Oct-26 09:36	308.56	277.70	308.56	100%	90%	-13
HVAC WORK		106	06-May-26 08:00	08-Jul-26 17:00	06-May-26 08:00 A	02-Oct-26 09:36 A	5,457.24	5,457.24	5,457.24	100%	100%	-72
PG-Q-PR-SL-AC-DL-10	Split Air Conditioning Unit(Completed)	39	06-May-26 08:00	24-Jun-26 17:00	06-May-26 08:00 A	24-Jun-26 17:00 A	1,673.62	1,673.62	1,673.62	100%	100%	0
PG-Q-PR-SL-AC-DL-10_R	Split Air Conditioning Unit(Remaining)	12	25-Jun-26 08:00	08-Jul-26 17:00	27-Aug-26 08:00 A	02-Oct-26 09:36 A	1,115.75	1,115.75	1,115.75	100%	100%	-18
PG-Q-PR-SL-AC-DL-20	Air Duct(Completed)	39	06-May-26 08:00	24-Jun-26 17:00	06-May-26 08:00 A	24-Jun-26 17:00 A	842.40	842.40	842.40	100%	100%	0
PG-Q-PR-SL-AC-DL-20_R	Air Duct(Remaining)	12	25-Jun-26 08:00	08-Jul-26 17:00	27-Aug-26 08:00 A	02-Oct-26 09:36 A	561.60	561.60	561.60	100%	100%	-18
PG-Q-PR-SL-AC-DL-30	Diffusers and Grills(Completed)	39	06-May-26 08:00	24-Jun-26 17:00	06-May-26 08:00 A	24-Jun-26 17:00 A	401.27	401.27	401.27	100%	100%	0
PG-Q-PR-SL-AC-DL-30_R	Diffusers and Grills(Remaining)	12	25-Jun-26 08:00	08-Jul-26 17:00	27-Aug-26 08:00 A	02-Oct-26 09:36 A	267.52	267.52	267.52	100%	100%	-18
PG-Q-PR-SL-AC-DL-40	Exhaust fans(Completed)	39	06-May-26 08:00	24-Jun-26 17:00	06-May-26 08:00 A	24-Jun-26 17:00 A	357.05	357.05	357.05	100%	100%	0
PG-Q-PR-SL-AC-DL-40_R	Exhaust fans(Remaining)	12	25-Jun-26 08:00	08-Jul-26 17:00	27-Aug-26 08:00 A	02-Oct-26 09:36 A	238.03	238.03	238.03	100%	100%	-18
PLUMBING WORK		7	06-May-26 08:00	13-May-26 17:00	06-May-26 08:00 A	13-May-26 17:00 A	28,323.27	28,323.27	28,323.27	100%	100%	0
PG-Q-PR-SL-PB-DL-10	PPR Pipes & Valves	7	06-May-26 08:00	13-May-26 17:00	06-May-26 08:00 A	13-May-26 17:00 A	2,386.80	2,386.80	2,386.80	100%	100%	0
PG-Q-PR-SL-PB-DL-20	UPCV Pipes	7	06-May-26 08:00	13-May-26 17:00	06-May-26 08:00 A	13-May-26 17:00 A	3,016.71	3,016.71	3,016.71	100%	100%	0
PG-Q-PR-SL-PB-DL-30	Sanitary Drainage Fixtures	7	06-May-26 08:00	13-May-26 17:00	06-May-26 08:00 A	13-May-26 17:00 A	22,919.76	22,919.76	22,919.76	100%	100%	0
IRRIGATION WORK		101	06-May-26 08:00	08-Jul-26 17:00	06-May-26 08:00 A	25-Oct-26 09:36	118,531.08	111,419.22	118,531.08	100%	94%	-91
PG-Q-PR-SL-IR-DL-10	Gate Valve including valve box(Completed)	39	06-May-26 08:00	24-Jun-26 17:00	06-May-26 08:00 A	24-Jun-26 17:00 A	4,790.66	4,790.66	4,790.66	100%	100%	0
PG-Q-PR-SL-IR-DL-10_R	Gate Valve including valve box(Remaining)	12	25-Jun-26 08:00	08-Jul-26 17:00	14-Aug-26 08:00 A	25-Oct-26 09:36	7,186.00	6,467.40	7,186.00	100%	90%	-48
PG-Q-PR-SL-IR-DL-20	Bubblers and Spreyers(Completed)	39	06-May-26 08:00	24-Jun-26 17:00	06-May-26 08:00 A	24-Jun-26 17:00 A	42,621.77	42,621.77	42,621.77	100%	100%	0
PG-Q-PR-SL-IR-DL-20_R	Bubblers and Spreyers(Remaining)	12	25-Jun-26 08:00	08-Jul-26 17:00	20-Aug-26 08:00 A	25-Oct-26 09:36	63,932.65	57,539.39	63,932.65	100%	90%	-43
ELECTRICAL WORK		128	11-May-26 08:00	12-Jul-26 17:00	11-May-26 08:00 A	25-Oct-26 12:00	3,667.68	3,447.62	3,667.68	100%	94%	-89
PG-Q-PR-SL-EL-DL-10	Wiring Devices Materials(Completed)	35	11-May-26 08:00	24-Jun-26 17:00	11-May-26 08:00 A	24-Jun-26 17:00 A	1,467.07	1,467.07	1,467.07	100%	100%	0
PG-Q-PR-SL-EL-DL-10_R	Wiring Devices Materials(Remaining)	15	25-Jun-26 08:00	12-Jul-26 17:00	26-Sep-26 08:00 A	25-Oct-26 12:00	2,200.61	1,980.55	2,200.61	100%	90%	-11
FIRE FIGHTING WORK		129	06-May-26 08:00	08-Jul-26 17:00	06-May-26 08:00 A	25-Oct-26 09:36	204.39	192.13	204.39	100%	94%	-91
PG-Q-PR-SL-FF-DL-10	Fire Extinguishers(Completed)	39	06-May-26 08:00	24-Jun-26 17:00	06-May-26 08:00 A	24-Jun-26 17:00 A	81.76	81.76	81.76	100%	100%	0
PG-Q-PR-SL-FF-DL-10_R	Fire Extinguishers(Remaining)	12	25-Jun-26 08:00	08-Jul-26 17:00	26-Sep-26 08:00 A	25-Oct-26 09:36	122.63	110.37	122.63	100%	90%	-13
CONSTRUCTION STAGE		259	24-Mar-26 08:00	16-Dec-26 17:00	24-Mar-26 08:00 A	25-Jan-27 15:24	9,229,811.49	7,250,040.43	10,522,524.00	87.71%	68.9%	-34
PLAYGROUND AND LANDSCAPING WORKS		246	24-Mar-26 08:00	16-Dec-26 17:00	24-Mar-26 08:00 A	03-Jan-27 17:00	5,507,994.11	5,480,031.42	6,019,638.42	91.5%	91.04%	-15
CUT AND FILL		38	24-Mar-26 08:00	06-May-26 17:00	24-Mar-26 08:00 A	06-May-26 17:00 A	900,600.00	900,600.00	900,600.00	100%	100%	0
PG-Q-CON-EX-CF-10	Existing Soil Excavation Works	36	24-Mar-26 08:00	04-May-26 17:00	24-Mar-26 08:00 A	04-May-26 17:00 A	233,280.00	233,280.00	233,280.00	100%	100%	0
PG-Q-CON-EX-CF-20	Soil Replacement Works	27	05-Apr-26 08:00	05-May-26 17:00	05-Apr-26 08:00 A	05-May-26 17:00 A	171,600.00	171,600.00	171,600.00	100%	100%	0
PG-Q-CON-EX-CF-30	Levelling & Backfilling Works	18	16-Apr-26 08:00	06-May-26 17:00	16-Apr-26 08:00 A	06-May-26 17:00 A	495,720.00	495,720.00	495,720.00	100%	100%	0
PLAYGROUND WORKS		198	21-Apr-26 08:00	02-Dec-26 17:00	21-Apr-26 08:00 A	14-Dec-26 10:48	1,219,061.19	1,225,919.75	1,318,471.20	92.46%	92.98%	-9
FOOTBALL PLAYGROUND WORKS		172	21-Apr-26 08:00	17-Nov-26 17:00	21-Apr-26 08:00 A	12-Nov-26 12:48	585,918.56	572,933.63	611,282.16	95.85%	93.73%	4
PG-Q-CON-EX-FB-10	Subgrade Preparation and Compaction	14	21-Apr-26 08:00	06-May-26 16:12	21-Apr-26 08:00 A	06-May-26 16:12 A	23,667.00	23,667.00	23,667.00	100%	100%	0
PG-Q-CON-EX-FB-100	Markings and Signages	8	09-Nov-26 08:00	17-Nov-26 17:00	03-Nov-26 12:48	12-Nov-26 12:48	0.00	0.00	23,667.00	0%	0%	0
PG-Q-CON-EX-FB-110	Install Playground Benches	17	20-Oct-26 08:00	08-Nov-26 17:00	27-Aug-26 08:00 A	03-Nov-26 12:48	363.56	1,648.13	2,060.16	17.65%	80%	-41
PG-Q-CON-EX-FB-120	Installation of Lighting System	12	19-Aug-26 08:00	01-Sep-26 17:00	20-Aug-26 08:00 A	25-Oct-26 09:36	24,360.00	21,924.00	24,360.00	100%	90%	-43
PG-Q-CON-EX-FB-20	Sub-Base Laying and Compaction	10	26-Apr-26 08:00	06-May-26 17:00	26-Apr-26 08:00 A	06-May-26 17:00 A	23,667.00	23,667.00	23,667.00	100%	100%	0
PG-Q-CON-EX-FB-30	Base Course Laying and Compaction	33	06-May-26 08:00	17-Jun-26 17:00	06-May-26 08:00 A	17-Jun-26 17:00 A	23,667.00	23,667.00	23,667.00	100%	100%	0
PG-Q-CON-EX-FB-40	Tartan flooring(Completed)	7	17-Jun-26 08:00	24-Jun-26 17:00	17-Jun-26 08:00 A	24-Jun-26 17:00 A	104,457.60	104,457.60	104,457.60	100%	100%	0
PG-Q-CON-EX-FB-40_R	Tartan flooring(Remaining)	15	14-Sep-26 08:00	01-Oct-26 17:00	12-Jul-26 08:00 A	14-Aug-26 17:00 A	243,734.40	243,734.40	243,734.40	100%	100%	-14
PG-Q-CON-EX-FB-50	Goal Post Foundation	25	21-Jul-26 08:00	18-Aug-26 17:00	06-Aug-26 08:00 A	27-Aug-26 17:00 A	35,500.50	35,500.50	35,500.50	100%	100%	6
PG-Q-CON-EX-FB-60	Goal Post Installation & Alignment	15	03-Oct-26 08:00	19-Oct-26 17:00	27-Aug-26 08:00 A	31-Oct-26 09:36	35,500.50	28,400.40	35,500.50	100%	80%	-39

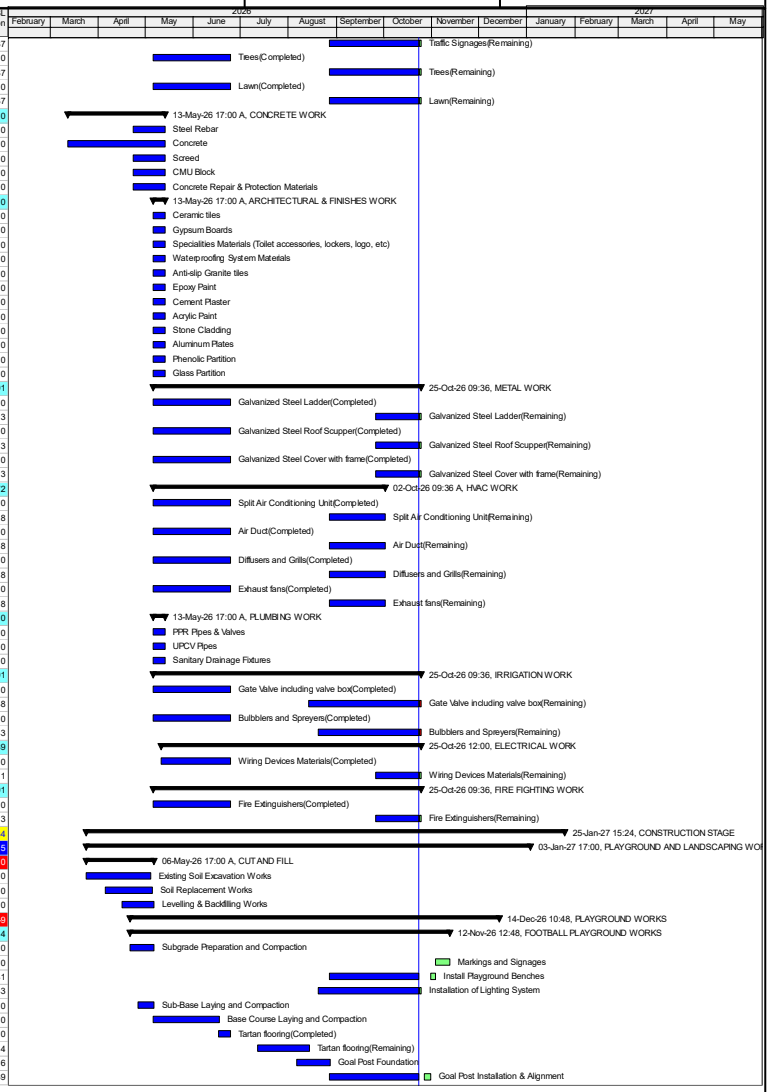


Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining W...
Milestone
summary

Baseline Schedule Rev.00

PLAYGROUNDS INITIATIVE - QASSIM, HAIL & TABUK - 25-Oct-2026

Activity ID	Activity Name	O.D	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Schedule % Complete	Performance % Complete	Variance - BL Project Duration
PG-Q-CON-EX-FB-70	Topsoil Placement	12	07-Jul-26 08:00	20-Jul-26 17:00	12-Jul-26 08:00 A	14-Aug-26 17:00 A	23,667.00	23,667.00	23,667.00	100%	100%	-17
PG-Q-CON-EX-FB-80	Fine Grading & Leveling	10	25-Jun-26 08:00	06-Jul-26 17:00	09-Jul-26 08:00 A	11-Jul-26 17:00 A	23,667.00	23,667.00	23,667.00	100%	100%	8
PG-Q-CON-EX-FB-90	Turfing / Seeding Works	10	02-Sep-26 08:00	13-Sep-26 17:00	14-Aug-26 08:00 A	27-Oct-26 09:36	23,667.00	18,933.60	23,667.00	100%	80%	-52
BASKETBALL PLAYGROUND WORKS		163	30-Apr-26 08:00	17-Nov-26 17:00	30-Apr-26 08:00 A	09-Nov-26 09:12	377,079.59	373,064.98	381,705.12	98.79%	97.74%	8
PG-Q-CON-EX-BB-10	Subgrade Preparation and Compaction	6	30-Apr-26 08:00	06-May-26 16:12	30-Apr-26 08:00 A	06-May-26 16:12 A	15,472.08	15,472.08	15,472.08	100%	100%	0
PG-Q-CON-EX-BB-100	Install Playground Benches	18	28-Oct-26 08:00	17-Nov-26 17:00	27-Sep-26 08:00 A	09-Nov-26 09:12	0.00	1,236.10	1,545.12	0%	80%	-19
PG-Q-CON-EX-BB-20	Sub-Base Laying and Compaction	1	05-May-26 16:12	06-May-26 17:00	05-May-26 16:12 A	06-May-26 17:00 A	15,472.08	15,472.08	15,472.08	100%	100%	0
PG-Q-CON-EX-BB-30	Base Course Laying and Compaction	33	06-May-26 08:00	17-Jun-26 17:00	06-May-26 08:00 A	17-Jun-26 17:00 A	15,472.08	15,472.08	15,472.08	100%	100%	0
PG-Q-CON-EX-BB-40	Tartan flooring	17	11-Aug-26 08:00	30-Aug-26 17:00	30-Jul-26 08:00 A	14-Aug-26 17:00 A	261,144.00	261,144.00	261,144.00	100%	100%	4
PG-Q-CON-EX-BB-50	Basketball Pole Foundation	25	25-Jun-26 08:00	23-Jul-26 17:00	06-Aug-26 08:00 A	13-Aug-26 17:00 A	15,472.08	15,472.08	15,472.08	100%	100%	18
PG-Q-CON-EX-BB-60	Basketball Pole Installation & Alignment	17	17-Sep-26 08:00	07-Oct-26 17:00	20-Aug-26 08:00 A	01-Nov-26 09:12	15,472.08	12,377.66	15,472.08	100%	80%	-44
PG-Q-CON-EX-BB-70	Floor Surface Curing(Completed)	7	17-Jun-26 08:00	24-Jun-26 17:00	17-Jun-26 08:00 A	24-Jun-26 17:00 A	4,641.62	4,641.62	4,641.62	100%	100%	0
PG-Q-CON-EX-BB-70_R	Floor Surface Curing(Remaining)	15	25-Jul-26 08:00	10-Aug-26 17:00	06-Aug-26 08:00 A	14-Aug-26 17:00 A	10,830.46	10,830.46	10,830.46	100%	100%	8
PG-Q-CON-EX-BB-80	Court Line Marking	15	31-Aug-26 08:00	16-Sep-26 17:00	20-Aug-26 08:00 A	27-Oct-26 15:00	13,091.76	10,473.41	13,091.76	100%	80%	-43
PG-Q-CON-EX-BB-90	Backboard & Hoop Installation	17	08-Oct-26 08:00	27-Oct-26 17:00	01-Oct-26 11:12 A	04-Nov-26 12:24	10,011.35	10,473.41	13,091.76	76.47%	80%	-12
PADEL PLAYGROUND WORKS		185	06-May-26 08:00	02-Dec-26 17:00	06-May-26 08:00 A	14-Dec-26 10:48	256,063.05	279,921.14	325,483.92	78.67%	86%	-9
PG-Q-CON-EX-PD-10	Excavation For Fence Footing(Completed)	39	06-May-26 08:00	24-Jun-26 17:00	06-May-26 08:00 A	24-Jun-26 17:00 A	16,243.20	16,243.20	16,243.20	100%	100%	0
PG-Q-CON-EX-PD-10_R	Excavation For Fence Footing(Remaining)	7	25-Jun-26 08:00	02-Jul-26 17:00	06-Aug-26 08:00 A	14-Aug-26 17:00 A	1,804.80	1,804.80	1,804.80	100%	100%	0
PG-Q-CON-EX-PD-20	RC Foundations For Fence(Completed)	27	20-May-26 08:00	24-Jun-26 17:00	20-May-26 08:00 A	24-Jun-26 17:00 A	1,767.48	1,767.48	1,767.48	100%	100%	0
PG-Q-CON-EX-PD-20_R	RC Foundations For Fence(Remaining)	20	04-Jul-26 08:00	26-Jul-26 17:00	07-Aug-26 08:00 A	27-Aug-26 17:00 A	1,767.48	1,767.48	1,767.48	100%	100%	2
PG-Q-CON-EX-PD-30	Tartan Flooring Layers(Completed)	7	17-Jun-26 08:00	24-Jun-26 17:00	17-Jun-26 08:00 A	24-Jun-26 17:00 A	130,572.00	130,572.00	130,572.00	100%	100%	0
PG-Q-CON-EX-PD-30_R	Tartan Flooring Layers(Remaining)	16	11-Oct-26 08:00	28-Oct-26 17:00	06-Aug-26 08:00 A	09-Nov-26 10:48	89,768.25	117,514.80	130,572.00	68.75%	90%	-64
PG-Q-CON-EX-PD-40	Steel Structure & Fence Supports Installation	18	11-Aug-26 08:00	31-Aug-26 17:00	20-Aug-26 08:00 A	28-Oct-26 10:48	3,534.96	2,827.97	3,534.96	100%	80%	-40
PG-Q-CON-EX-PD-50	Tempered Glass Installation	17	20-Sep-26 08:00	10-Oct-26 17:00	12-Oct-26 08:00 A	09-Nov-26 10:48	5,302.44	3,181.46	5,302.44	100%	60%	-7
PG-Q-CON-EX-PD-60	Chain Link Fence & Gates Installation	16	01-Sep-26 08:00	19-Sep-26 17:00	20-Aug-26 08:00 A	01-Nov-26 12:24	5,302.44	4,241.95	5,302.44	100%	80%	-46
PG-Q-CON-EX-PD-70	Court Accessories Installation	15	29-Oct-26 08:00	15-Nov-26 17:00	09-Nov-26 10:48	26-Nov-26 10:48	0.00	0.00	27,072.00	0%	0%	0
PG-Q-CON-EX-PD-80	Install Playground Benches	15	16-Nov-26 08:00	02-Dec-26 17:00	26-Nov-26 10:48	14-Dec-26 10:48	0.00	0.00	1,545.12	0%	0%	0
GENERAL SITE WORKS		226	16-Apr-26 08:00	16-Dec-26 17:00	16-Apr-26 08:00 A	03-Jan-27 17:00	1,526,282.82	1,415,562.43	1,617,941.82	94.33%	87.49%	-15
FENCE WORKS		168	16-Apr-26 08:00	13-Sep-26 17:00	16-Apr-26 08:00 A	20-Oct-26 17:00 A	32,909.40	32,909.40	32,909.40	100%	100%	-31
PG-Q-CON-EX-GN-FN-10	Excavation for fence foundation	3	16-Apr-26 08:00	19-Apr-26 17:00	16-Apr-26 08:00 A	19-Apr-26 17:00 A	6,581.88	6,581.88	6,581.88	100%	100%	0
PG-Q-CON-EX-GN-FN-20	Concrete Foundations for Fence	10	21-Jul-26 08:00	01-Aug-26 17:00	13-Aug-26 08:00 A	20-Aug-26 17:00 A	6,581.88	6,581.88	6,581.88	100%	100%	3
PG-Q-CON-EX-GN-FN-30	Installation of Galvanized Steel Posts & Framing	12	02-Aug-26 08:00	15-Aug-26 17:00	20-Aug-26 08:00 A	17-Oct-26 17:00 A	6,581.88	6,581.88	6,581.88	100%	100%	-37
PG-Q-CON-EX-GN-FN-40	Fixing of Chain Link Mesh, Tensioning & Bracing	15	16-Aug-26 08:00	01-Sep-26 17:00	27-Sep-26 15:24 A	19-Oct-26 17:00 A	6,581.88	6,581.88	6,581.88	100%	100%	-4
PG-Q-CON-EX-GN-FN-50	Installation of Gates	10	02-Sep-26 08:00	13-Sep-26 17:00	14-Oct-26 08:00 A	20-Oct-26 17:00 A	6,581.88	6,581.88	6,581.88	100%	100%	4
MECHANICAL WORK		159	12-May-26 08:00	18-Aug-26 17:00	12-May-26 08:00 A	19-Nov-26 11:12	780,707.34	707,170.08	780,707.34	100%	90.58%	-78
STORM WATER AND UTILITY WORK		157	12-May-26 08:00	16-Aug-26 17:00	12-May-26 08:00 A	17-Nov-26 11:12	27,252.00	19,573.20	27,252.00	100%	71.82%	-78
PG-Q-CON-EX-GN-M-10	Excavation	2	12-May-26 08:00	13-May-26 17:00	12-May-26 08:00 A	13-May-26 17:00 A	3,096.00	3,096.00	3,096.00	100%	100%	0
PG-Q-CON-EX-GN-M-20	Bedding preparation & level control(Completed)	27	20-May-26 08:00	24-Jun-26 17:00	20-May-26 08:00 A	24-Jun-26 17:00 A	1,651.20	1,651.20	1,651.20	100%	100%	0
PG-Q-CON-EX-GN-M-20_R	Bedding preparation & level control(Remaining)	8	25-Jun-26 08:00	04-Jul-26 17:00	07-Aug-26 08:00 A	27-Aug-26 17:00 A	412.80	412.80	412.80	100%	100%	-10
PG-Q-CON-EX-GN-M-30	Manhole Installation(Completed)	7	17-Jun-26 08:00	24-Jun-26 17:00	17-Jun-26 08:00 A	24-Jun-26 17:00 A	1,032.00	1,032.00	1,032.00	100%	100%	0
PG-Q-CON-EX-GN-M-30_R	Manhole Installation(Remaining)	6	05-Jul-26 08:00	11-Jul-26 17:00	20-Aug-26 08:00 A	24-Oct-26 12:48	4,128.00	3,715.20	4,128.00	100%	90%	-49
PG-Q-CON-EX-GN-M-40	150 mm uPVC pipe laying & jointing	6	12-Jul-26 08:00	18-Jul-26 17:00	20-Aug-26 08:00 A	25-Oct-26 09:36	10,740.00	9,666.00	10,740.00	100%	90%	-49
PG-Q-CON-EX-GN-M-50	Concrete Encasement	7	19-Jul-26 08:00	26-Jul-26 17:00	25-Oct-26 09:36	02-Nov-26 09:36	2,064.00	0.00	2,064.00	100%	0%	0
PG-Q-CON-EX-GN-M-60	Backfilling & Compaction	6	27-Jul-26 08:00	02-Aug-26 17:00	02-Nov-26 09:36	09-Nov-26 09:36	2,064.00	0.00	2,064.00	100%	0%	0
PG-Q-CON-EX-GN-M-70	Surface Reinstatement & Civil Works	6	10-Aug-26 08:00	16-Aug-26 17:00	10-Nov-26 11:12	17-Nov-26 11:12	2,064.00	0.00	2,064.00	100%	0%	0
IRRIGATION SYSTEM WORKS		86	17-Jun-26 08:00	09-Aug-26 17:00	17-Jun-26 08:00 A	10-Nov-26 11:12	753,137.40	687,596.88	753,137.40	100%	91.3%	-78
PG-Q-CON-EX-GN-M-100	Installation of Bubblers and Sprinklers	3	06-Aug-26 08:00	09-Aug-26 17:00	27-Aug-26 08:00 A	10-Nov-26 11:12	236,787.60	189,430.08	236,787.60	100%	80%	-60
PG-Q-CON-EX-GN-M-80	Installation of HDPE Irrigation Pipe Network with Gate Valve and	7	17-Jun-26 08:00	24-Jun-26 17:00	17-Jun-26 08:00 A	24-Jun-26 17:00 A	148,902.18	148,902.18	148,902.18	100%	100%	0
PG-Q-CON-EX-GN-M-80_R	Installation of HDPE Irrigation Pipe Network with Gate Valve and	3	30-Jul-26 08:00	02-Aug-26 17:00	06-Aug-26 08:00 A	01-Oct-26 11:12 A	276,532.62	276,532.62	276,532.62	100%	100%	-44
PG-Q-CON-EX-GN-M-90	Installation of Irrigation Control System	3	03-Aug-26 08:00	05-Aug-26 17:00	20-Aug-26 08:00 A	09-Nov-26 15:24	90,915.00	72,732.00	90,915.00	100%	80%	-66
FIRE PROTECTION SYSTEM		2	17-Aug-26 08:00	18-Aug-26 17:00	17-Nov-26 11:12	19-Nov-26 11:12	317.94	0.00	317.94	100%	0%	0
PG-Q-CON-EX-GN-M-110	Fire Extinguisher Installation	2	17-Aug-26 08:00	18-Aug-26 17:00	17-Nov-26 11:12	19-Nov-26 11:12	317.94	0.00	317.94	100%	0%	0
ELECTRICAL WORK		197	20-May-26 08:00	01-Nov-26 17:00	20-May-26 08:00 A	14-Dec-26 09:36	692,767.08	582,802.15	693,965.28	99.83%	83.98%	-36
POWER, LIGHTING & GROUNDING		162	20-May-26 08:00	20-Sep-26 17:00	20-May-26 08:00 A	28-Nov-26 09:36	636,895.08	548,560.03	636,895.08	100%	86.13%	-57
PG-Q-CON-EX-GN-E-10	Excavation(Completed)	27	20-May-26 08:00	24-Jun-26 17:00	20-May-26 08:00 A	24-Jun-26 17:00 A	121,836.96	121,836.96	121,836.96	100%	100%	0
PG-Q-CON-EX-GN-E-10_R	Excavation(Remaining)	3	13-Aug-26 08:00	16-Aug-26 17:00	16-Jul-26 08:00 A	27-Aug-26 17:00 A	52,215.84	52,215.84	52,215.84	100%	100%	-34
PG-Q-CON-EX-GN-E-20	Foundation Work for Site Lighting Poles(Completed)	13	10-Jun-26 08:00	24-Jun-26 17:00	10-Jun-26 08:00 A	24-Jun-26 17:00 A	69,621.12	69,621.12	69,621.12	100%	100%	0
PG-Q-CON-EX-GN-E-20_R	Foundation Work for Site Lighting Poles(Remaining)	4	13-Aug-26 08:00	17-Aug-26 17:00	20-Aug-26 08:00 A	18-Nov-26 08:48	162,449.28	129,959.42	162,449.28	100%	80%	-72
PG-Q-CON-EX-GN-E-30	Lightning Protection System (LPS)	3	29-Aug-26 08:00	31-Aug-26 17:00	27-Aug-26 08:00 A	19-Nov-26 17:00	8,265.00	6,612.00	8,265.00	100%	80%	-69
PG-Q-CON-EX-GN-E-40	KWH Meter and MDB Installation	2	01-Sep-26 08:00	02-Sep-26 17:00	13-Oct-26 08:00 A	21-Nov-26 15:24	4,586.70	2,752.02	4,586.70	100%	60%	-32
PG-Q-CON-EX-GN-E-50	Power Panels and Distribution Boards	5	03-Sep-26 08:00	08-Sep-26 17:00	14-Oct-26 08:00 A	23-Nov-26 15:24	17,397.90	10,438.74	17,397.90	100%	60%	-30
PG-Q-CON-EX-GN-E-60	Site Lighting Poles Installation	3	09-Sep-26 08:00	12-Sep-26 17:00	20-Aug-26 08:00 A	24-Nov-26 11:12	174,052.80	139,242.24	174,052.80	100%	80%	-78
PG-Q-CON-EX-GN-E-70	Wiring Works	3	13-Sep-26 08:00	15-Sep-26 17:00	10-Oct-26 08:00 A	25-Nov-26 12:48	4,224.00	2,534.40	4,224.00	100%	60%	-38
PG-Q-CON-EX-GN-E-80	Lighting Fixtures with outlets Installation	4	16-Sep-26 08:00	20-Sep-26 17:00	12-Oct-26 08:00 A	28-Nov-26 09:36	22,245.48	13,347.29	22,245.48	100%	60%	-36
ELV SYSTEMS (TELECOM, DATA, AV & CCTV)		25	21-Sep-26 08:00	20-Oct-26 17:00	07-Oct-26 08:00 A	09-Dec-26 09:36	43,146.00	25,887.60	43,146.00	100%	60%	-29
PG-Q-CON-EX-GN-E-100	Fiber Optic Pull Box Installation	3	26-Sep-26 08:00	28-Sep-26 17:00	10-Oct-26 08:00 A	30-Nov-26 12:48	619.80	371.88	619.80	100%	60%	-42
PG-Q-CON-EX-GN-E-110	Telephone and Data Outlet Installation	4	29-Sep-26 08:00	03-Oct-26 17:00	10-Oct-26 08:00 A	02-Dec-26 09:36	3,718.80	2,231.28	3,718.80	100%	60%	-42
PG-Q-CON-EX-GN-E-120	Telecom Equipment and AV HDMI Installation	4	04-Oct-26 08:00	07-Oct-26 17:00	12-Oct-26 08:00 A	03-Dec-26 15:24	15,249.12	9,149.47	15,249.12	100%	60%	-42
PG-Q-CON-EX-GN-E-130	CCTV Rack / Cabinet Installation	4	08-Oct-26 08:00	12-Oct-26 17:00	11-Oct-26 08:00 A	06-Dec-26 11:12	1,446.48	867.89	1,446.48	100%	60%	-44
PG-Q-CON-EX-GN-E-140	NVR and CCTV Monitor Installation	4	13-Oct-26 08:00	17-Oct-26 17:00	13-Oct-26 08:00 A	07-Dec-26 17:00	6,612.00	3,967.20	6,612.00	100%	60%	-44
PG-Q-CON-EX-GN-E-150	IP Camera Installation	3	18-Oct-26 08:00	20-Oct-26 17:00	14-Oct-26 08:00 A	09-Dec-26 09:36	14,880.00	8,928.00	14,880.00	100%	60%	-45
PG-Q-CON-EX-GN-E-90	ELV Containment & Cabling Works	3	21-Sep-26 08:00	24-Sep-26 17:00	07-Oct-26 08:00 A	29-Nov-26 11:12	619.80	371.88	619.80	100%	60%	-42
FIRE ALARM SYSTEM		32	26-Sep-26 08:00	01-Nov-26 17:00	11-Oct-26 08:00 A	14-Dec-26 09:36	12,726.00	8,354.52	13,924.20	91.39%	60%	-23

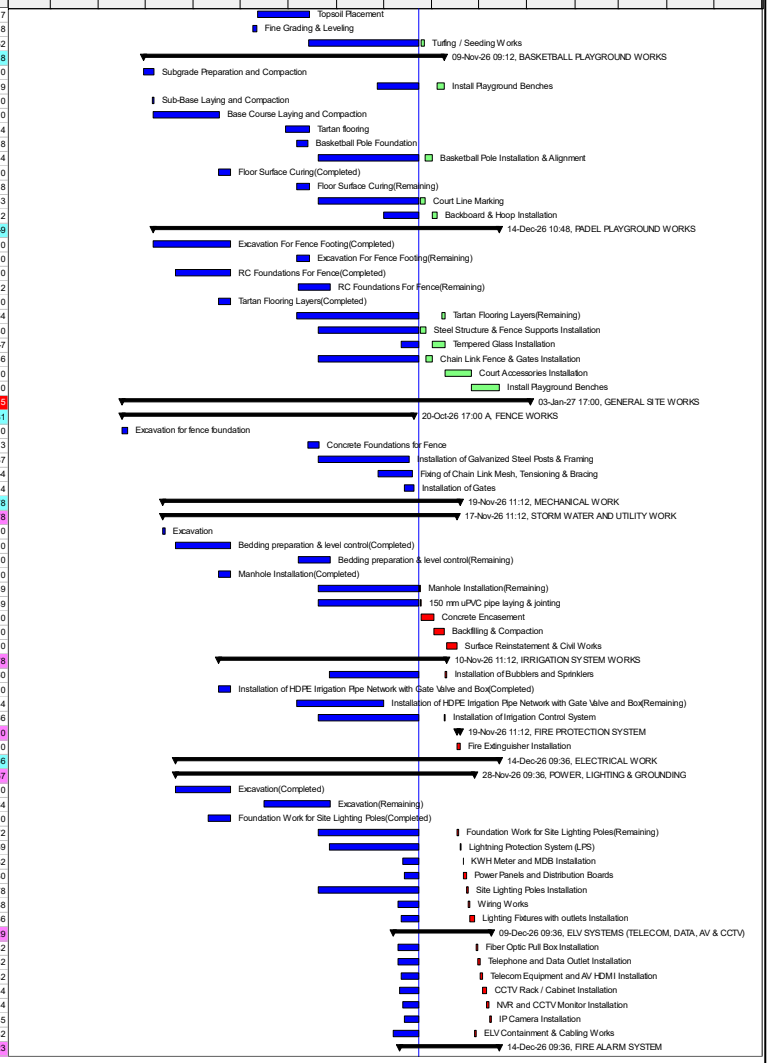


Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining W...
Milestone
summary

Baseline Schedule Rev.00

PLAYGROUNDS INITIATIVE - QASSIM, HAIL & TABUK - 25-Oct-2026

Activity ID	Activity Name	O.D	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Schedule % Complete	Performance % Complete	Variance - BL Project Duration
PG-Q-CON-EXG-NE-160	Fire Alarm Containment & Cabling	8	26-Sep-26 08:00	04-Oct-26 17:00	11-Oct-26 08:00 A	02-Dec-26 12:48	1,983.60	1,190.16	1,983.60	100%	60%	-38
PG-Q-CON-EXG-NE-170	Fire Alarm Control Panel (FACP) Installation	8	05-Oct-26 08:00	13-Oct-26 17:00	12-Oct-26 08:00 A	06-Dec-26 15:24	2,644.80	1,586.88	2,644.80	100%	60%	-40
PG-Q-CON-EXG-NE-180	Initiating Devices (Detectors & Manual Pull Station)	8	14-Oct-26 08:00	22-Oct-26 17:00	13-Oct-26 08:00 A	09-Dec-26 17:00	8,097.60	4,858.56	8,097.60	100%	60%	-42
PG-Q-CON-EXG-NE-190	Notification Appliances (Stobe with Sounder)	8	24-Oct-26 08:00	01-Nov-26 17:00	15-Oct-26 08:00 A	14-Dec-26 09:36	0.00	718.92	1,198.20	0%	60%	-43
PARKING WORK		157	17-Jun-26 08:00	09-Nov-26 17:00	17-Jun-26 08:00 A	15-Dec-26 09:36	19,899.00	88,440.00	102,919.80	19.33%	85.93%	-30
PG-Q-CON-EXG-NPR-10	Installation of Parking Accessories	5	29-Oct-26 08:00	03-Nov-26 17:00	20-Aug-26 08:00 A	01-Oct-26 15:00 A	0.00	44,220.00	44,220.00	0%	100%	-31
PG-Q-CON-EXG-NPR-20	Interlock tiles(Completed)	7	17-Jun-26 08:00	24-Jun-26 17:00	17-Jun-26 08:00 A	24-Jun-26 17:00 A	19,899.00	19,899.00	19,899.00	100%	100%	0
PG-Q-CON-EXG-NPR-20_R	Interlock tiles(Remaining)	3	01-Nov-26 08:00	03-Nov-26 17:00	06-Jul-26 10:00 A	10-Jul-26 17:00 A	0.00	24,321.00	24,321.00	0%	100%	-1
PG-Q-CON-EXG-NPR-30	Marking & Signages	5	04-Nov-26 08:00	09-Nov-26 17:00	09-Dec-26 09:36	15-Dec-26 09:36	0.00	0.00	14,479.80	0%	0%	0
SERVICE CONNECTION		38	10-Nov-26 08:00	16-Dec-26 17:00	12-Jul-26 08:00 A	03-Jan-27 17:00	0.00	4,240.80	7,440.00	0%	57%	-118
PG-Q-CON-EXG-SC-10	Excavation & Tiench Preparation	8	10-Nov-26 08:00	18-Nov-26 17:00	12-Jul-26 08:00 A	20-Aug-26 17:00 A	0.00	2,232.00	2,232.00	0%	100%	-27
PG-Q-CON-EXG-NSC-20	HDPE Pipe Laying & Valve Installation	8	19-Nov-26 08:00	28-Nov-26 17:00	14-Aug-26 08:00 A	15-Dec-26 17:00	0.00	2,008.80	2,232.00	0%	90%	-97
PG-Q-CON-EXG-NSC-30	Connection to City Network	8	29-Nov-26 08:00	07-Dec-26 17:00	16-Dec-26 08:00	24-Dec-26 17:00	0.00	0.00	1,488.00	0%	0%	0
PG-Q-CON-EXG-NSC-40	Backfilling	8	08-Dec-26 08:00	16-Dec-26 17:00	26-Dec-26 08:00	03-Jan-27 17:00	0.00	0.00	1,488.00	0%	0%	0
LANDSCAPING WORKS		168	31-May-26 08:00	14-Dec-26 17:00	30-May-26 08:48 A	26-Nov-26 14:36	1,813,759.70	1,900,072.74	2,134,335.00	84.98%	89.02%	15
HARDSCAPE WORK		168	31-May-26 08:00	14-Dec-26 17:00	30-May-26 08:48 A	26-Nov-26 14:36	1,644,359.70	1,692,172.74	1,712,409.00	96.03%	98.82%	15
PG-Q-CON-EXL-HS-10	Curbstone Installation(Completed)	22	31-May-26 08:00	24-Jun-26 17:00	30-May-26 08:48 A	24-Jun-26 17:00 A	604,590.00	604,590.00	604,590.00	100%	100%	0
PG-Q-CON-EXL-HS-10_R	Curbstone Installation(Remaining)	10	02-Sep-26 08:00	13-Sep-26 17:00	07-Jul-26 08:00 A	14-Aug-26 17:00 A	259,110.00	259,110.00	259,110.00	100%	100%	-23
PG-Q-CON-EXL-HS-20	Interlock Tiles Grey Scale with Black Marble Chips(Completed)	22	31-May-26 08:00	24-Jun-26 17:00	30-May-26 08:48 A	24-Jun-26 17:00 A	36,960.00	36,960.00	36,960.00	100%	100%	0
PG-Q-CON-EXL-HS-20_R	Interlock Tiles Grey Scale with Black Marble Chips(Remaining)	13	30-Sep-26 08:00	14-Oct-26 17:00	27-Aug-26 08:00 A	27-Oct-26 14:36	55,440.00	49,896.00	55,440.00	100%	90%	-39
PG-Q-CON-EXL-HS-30	Stamped Concrete Floor(Completed)	13	10-Jun-26 08:00	24-Jun-26 17:00	10-Jun-26 08:00 A	24-Jun-26 17:00 A	207,900.00	207,900.00	207,900.00	100%	100%	0
PG-Q-CON-EXL-HS-30_R	Stamped Concrete Floor(Remaining)	13	14-Sep-26 08:00	29-Sep-26 17:00	31-Jul-26 08:00 A	27-Aug-26 17:00 A	207,900.00	207,900.00	207,900.00	100%	100%	-11
PG-Q-CON-EXL-HS-40	Bike Path and Walking Path Construction(Completed)	22	31-May-26 08:00	24-Jun-26 17:00	30-May-26 08:48 A	24-Jun-26 17:00 A	146,025.00	146,025.00	146,025.00	100%	100%	0
PG-Q-CON-EXL-HS-40_R	Bike Path and Walking Path Construction(Remaining)	17	18-Jul-26 08:00	05-Aug-26 17:00	08-Jul-26 08:00 A	14-Aug-26 17:00 A	119,475.00	119,475.00	119,475.00	100%	100%	-15
PG-Q-CON-EXL-HS-50	Install Recycled Precast Concrete Seats(Completed)	7	17-Jun-26 08:00	24-Jun-26 17:00	17-Jun-26 08:00 A	24-Jun-26 17:00 A	6,959.70	6,959.70	6,959.70	100%	100%	0
PG-Q-CON-EXL-HS-50_R	Install Recycled Precast Concrete Seats(Remaining)	10	22-Nov-26 08:00	02-Dec-26 17:00	20-Aug-26 08:00 A	22-Nov-26 14:36	0.00	50,109.84	62,637.30	0%	80%	-70
PG-Q-CON-EXL-HS-60	Install Recycled Precast Concrete Trash Bins	10	03-Dec-26 08:00	14-Dec-26 17:00	12-Oct-26 08:00 A	26-Nov-26 14:36	0.00	3,247.20	5,412.00	0%	60%	-30
SOFTSCAPE WORK		139	10-Jun-26 08:00	21-Nov-26 17:00	10-Jun-26 08:00 A	19-Nov-26 14:36	169,400.00	207,900.00	421,926.00	40.15%	49.27%	1
PG-Q-CON-EXL-SS-10	Planting Trees	17	02-Nov-26 08:00	21-Nov-26 17:00	31-Oct-26 14:36	19-Nov-26 14:36	0.00	0.00	190,926.00	0%	0%	0
PG-Q-CON-EXL-SS-20	Lawn Area Preparation & Planting / Turfing(Completed)	13	10-Jun-26 08:00	24-Jun-26 17:00	10-Jun-26 08:00 A	24-Jun-26 17:00 A	115,500.00	115,500.00	115,500.00	100%	100%	0
PG-Q-CON-EXL-SS-20_R	Lawn Area Preparation & Planting / Turfing(Remaining)	15	15-Oct-26 08:00	01-Nov-26 17:00	27-Aug-26 08:00 A	31-Oct-26 14:36	53,900.00	92,400.00	115,500.00	46.67%	80%	-40
TANK WORKS		138	13-May-26 08:00	19-Aug-26 17:00	13-May-26 08:00 A	26-Oct-26 11:12	48,290.40	37,876.50	48,290.40	100%	78.43%	-56
SEPTIC TANK		33	13-May-26 08:00	24-Jun-26 17:00	13-May-26 08:00 A	24-Jun-26 17:00 A	7,475.22	7,475.22	7,475.22	100%	100%	0
PG-Q-CON-EXT-W-ST-10	Excavation	29	13-May-26 08:00	20-Jun-26 17:00	13-May-26 08:00 A	20-Jun-26 17:00 A	252.18	252.18	252.18	100%	100%	0
PG-Q-CON-EXT-W-ST-20	PCC / Lean Concrete laying	24	20-May-26 08:00	21-Jun-26 17:00	20-May-26 08:00 A	21-Jun-26 17:00 A	168.12	168.12	168.12	100%	100%	0
PG-Q-CON-EXT-W-ST-30	RCC Foundation	2	21-Jun-26 08:00	22-Jun-26 17:00	21-Jun-26 08:00 A	22-Jun-26 17:00 A	1,277.64	1,277.64	1,277.64	100%	100%	0
PG-Q-CON-EXT-W-ST-40	RCC Wall	4	20-Jun-26 08:00	23-Jun-26 17:00	20-Jun-26 08:00 A	23-Jun-26 17:00 A	2,757.60	2,757.60	2,757.60	100%	100%	0
PG-Q-CON-EXT-W-ST-50	RCC Slab	4	21-Jun-26 08:00	24-Jun-26 17:00	21-Jun-26 08:00 A	24-Jun-26 17:00 A	2,599.38	2,599.38	2,599.38	100%	100%	0
PG-Q-CON-EXT-W-ST-60	Finishing Work	3	22-Jun-26 08:00	24-Jun-26 17:00	22-Jun-26 08:00 A	24-Jun-26 17:00 A	252.18	252.18	252.18	100%	100%	0
PG-Q-CON-EXT-W-ST-70	Backfilling	2	23-Jun-26 08:00	24-Jun-26 17:00	23-Jun-26 08:00 A	24-Jun-26 17:00 A	168.12	168.12	168.12	100%	100%	0
WATER STORAGE TANK		138	13-May-26 08:00	19-Aug-26 17:00	13-May-26 08:00 A	26-Oct-26 11:12	40,815.18	30,401.28	40,815.18	100%	74.49%	-56
PG-Q-CON-EXT-W-IR-10	Excavation(Completed)	33	13-May-26 08:00	24-Jun-26 17:00	13-May-26 08:00 A	24-Jun-26 17:00 A	766.58	766.58	766.58	100%	100%	0
PG-Q-CON-EXT-W-IR-10_R	Excavation(Remaining)	7	25-Jun-26 08:00	02-Jul-26 17:00	07-Jul-26 08:00 A	08-Jul-26 17:00 A	85.18	85.18	85.18	100%	100%	5
PG-Q-CON-EXT-W-IR-20	RCC Foundation	15	04-Jul-26 08:00	20-Jul-26 17:00	09-Jul-26 08:00 A	26-Aug-26 17:00 A	4,136.40	4,136.40	4,136.40	100%	100%	-27
PG-Q-CON-EXT-W-IR-30	Backfilling	7	21-Jul-26 08:00	28-Jul-26 17:00	20-Aug-26 08:00 A	27-Aug-26 17:00 A	1,114.02	1,114.02	1,114.02	100%	100%	0
PG-Q-CON-EXT-W-IR-40	GRP Water Tank Installation	8	11-Aug-26 08:00	19-Aug-26 17:00	14-Oct-26 08:00 A	26-Oct-26 11:12	34,713.00	24,299.10	34,713.00	100%	70%	-2
AIR DOME CONSTRUCTION		216	13-May-26 08:00	26-Nov-26 17:00	13-May-26 08:00 A	25-Jan-27 15:24	3,396,773.00	1,461,181.68	4,178,041.20	81.3%	34.97%	-51
CIVIL WORK		155	13-May-26 08:00	10-Sep-26 17:00	13-May-26 08:00 A	15-Nov-26 15:24	1,711,669.97	1,210,693.39	1,711,669.97	100%	70.73%	-55
PG-Q-CON-EXA-D-CL-10	Excavation For Footing(Completed)	33	13-May-26 08:00	24-Jun-26 17:00	13-May-26 08:00 A	24-Jun-26 17:00 A	25,048.83	25,048.83	25,048.83	100%	100%	0
PG-Q-CON-EXA-D-CL-10_R	Excavation For Footing(Remaining)	6	09-Jul-26 08:00	15-Jul-26 17:00	09-Jul-26 08:00 A	10-Jul-26 17:00 A	225,439.46	225,439.46	225,439.46	100%	100%	5
PG-Q-CON-EXA-D-CL-20	Anti-Termite Treatment	2	16-Jul-26 08:00	18-Jul-26 17:00	11-Jul-26 08:00 A	12-Jul-26 17:00 A	83,496.10	83,496.10	83,496.10	100%	100%	0
PG-Q-CON-EXA-D-CL-30	PCC / Blinding Concrete	3	19-Jul-26 08:00	21-Jul-26 17:00	23-Jul-26 08:00 A	06-Aug-26 17:00 A	125,244.14	125,244.14	125,244.14	100%	100%	-10
PG-Q-CON-EXA-D-CL-40	RCC Foundation Works	12	22-Jul-26 08:00	04-Aug-26 17:00	31-Jul-26 08:00 A	13-Aug-26 17:00 A	250,488.29	250,488.29	250,488.29	100%	100%	0
PG-Q-CON-EXA-D-CL-50	Backfilling with Compaction	6	05-Aug-26 08:00	11-Aug-26 17:00	06-Aug-26 08:00 A	14-Aug-26 17:00 A	250,488.29	250,488.29	250,488.29	100%	100%	-1
PG-Q-CON-EXA-D-CL-60	Installation of Anchorage System	8	12-Aug-26 08:00	20-Aug-26 17:00	27-Aug-26 08:00 A	29-Sep-26 11:12 A	250,488.29	250,488.29	250,488.29	100%	100%	-19
PG-Q-CON-EXA-D-CL-70	Installation of Steel Cable Structural System	10	22-Aug-26 08:00	01-Sep-26 17:00	25-Oct-26 15:24	05-Nov-26 15:24	250,488.29	0.00	250,488.29	100%	0%	0
PG-Q-CON-EXA-D-CL-80	Installation of Membrane System	8	02-Sep-26 08:00	10-Sep-26 17:00	05-Nov-26 15:24	15-Nov-26 15:24	250,488.29	0.00	250,488.29	100%	0%	0
ARCHITECTURAL WORK		45	27-Oct-26 08:00	26-Nov-26 17:00	27-Aug-26 08:00 A	25-Jan-27 15:24	0.00	125,244.14	712,953.22	0%	17.57%	-102
PG-Q-CON-EXA-D-AR-10	Installation of Thermal Insulation System	8	27-Oct-26 08:00	04-Nov-26 17:00	27-Aug-26 08:00 A	03-Jan-27 15:24	0.00	125,244.14	250,488.29	0%	50%	-102
PG-Q-CON-EXA-D-AR-20	Installation of Doors & Access Systems	6	15-Nov-26 08:00	21-Nov-26 17:00	12-Jan-27 15:24	19-Jan-27 15:24	0.00	0.00	250,488.29	0%	0%	0
PG-Q-CON-EXA-D-AR-30	Installation of Logo	5	22-Nov-26 08:00	26-Nov-26 17:00	19-Jan-27 15:24	25-Jan-27 15:24	0.00	0.00	3,236.40	0%	0%	0
PG-Q-CON-EXA-D-AR-40	Final Fixing of Acessories & Finishes	8	05-Nov-26 08:00	14-Nov-26 17:00	03-Jan-27 15:24	12-Jan-27 15:24	0.00	0.00	208,740.24	0%	0%	0
MECHANICAL WORK		16	12-Sep-26 08:00	30-Sep-26 17:00	15-Nov-26 15:24	03-Dec-26 15:24	667,968.77	0.00	667,968.77	100%	0%	0
PG-Q-CON-EXA-D-ME-10	Installation of Main Air Package Units	5	12-Sep-26 08:00	16-Sep-26 17:00	15-Nov-26 15:24	21-Nov-26 15:24	250,488.29	0.00	250,488.29	100%	0%	0
PG-Q-CON-EXA-D-ME-20	Installation of Backup Air Package Unit	5	17-Sep-26 08:00	22-Sep-26 17:00	21-Nov-26 15:24	26-Nov-26 15:24	208,740.24	0.00	208,740.24	100%	0%	0
PG-Q-CON-EXA-D-ME-30	Installation of Complete HVAC System	6	24-Sep-26 08:00	30-Sep-26 17:00	26-Nov-26 15:24	03-Dec-26 15:24	208,740.24	0.00	208,740.24	100%	0%	0
ELECTRICAL WORK		90	17-Aug-26 08:00	26-Oct-26 17:00	27-Aug-26 08:00 A	29-Dec-26 15:24	1,017,134.26	125,244.14	1,085,449.25	93.71%	11.54%	-46
PG-Q-CON-EXA-D-EL-10	Installation of Electrical Boxes & MDBs	12	17-Aug-26 08:00	30-Aug-26 17:00	27-Aug-26 08:00 A	29-Oct-26 15:24	208,740.24	125,244.14	208,740.24	100%	60%	-42
PG-Q-CON-EXA-D-EL-20	Installation of Lighting System	12	31-Aug-26 08:00	13-Sep-26 17:00	29-Oct-26 15:24	12-Nov-26 15:24	208,740.24	0.00	208,740.24	100%	0%	0
PG-Q-CON-EXA-D-EL-30	Electrical Connections to Main Power Source (Excluding kWh Meter)	5	01-Oct-26 08:00	06-Oct-26 17:00	03-Dec-26 15:24	09-Dec-26 15:24	208,740.24	0.00	208,740.24	100%	0%	0
PG-Q-CON-EXA-D-EL-40	Installation of Backup Generator	6	07-Oct-26 08:00	13-Oct-26 17:00	09-Dec-26 15:24	16-Dec-26 15:24	208,740.24	0.00	208,740.24	100%	0%	0
PG-Q-CON-EXA-D-EL-50	Installation of Smart Dome System	11	14-Oct-26 08:00	26-Oct-26 17:00	16-Dec-26 15:24	29-Dec-26 15:24	182,173.30	0.00	250,488.29	72.73%	0%	0
TOILET BUILDING WORKS		163	06-May-26 08:00	20-Oct-26 17:00	06-May-26 08:00 A	31-Oct-26 10:24	324,844.38	308,827.33	324,844.38	100%	95.07%	-8

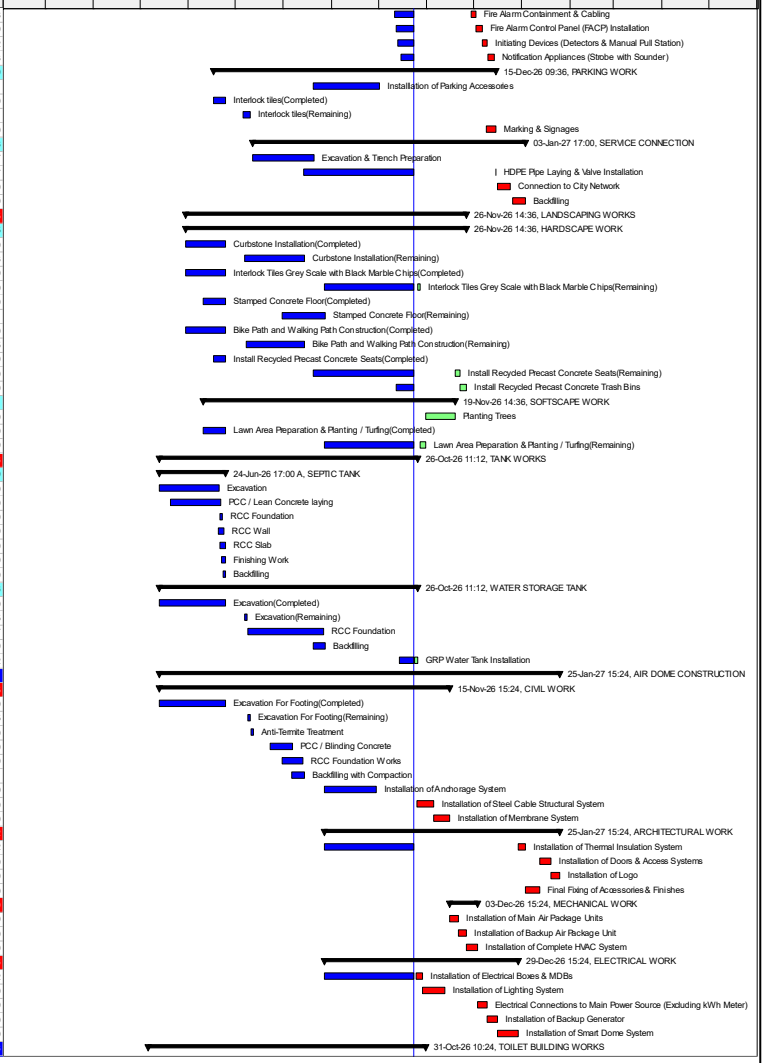

Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining W...
Milestone
summary

Baseline Schedule Rev.00

PLAYGROUNDS INITIATIVE - QASSIM, HAIL & TABUK - 25-Oct-2026

Activity ID	Activity Name	O.D	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Schedule % Complete	Performance % Complete	Variance - BL Project Duration
CIVIL WORK		162	06-May-26 08:00	19-Oct-26 17:00	06-May-26 08:00 A	29-Oct-26 17:00	227,117.58	214,414.56	227,117.58	100%	94.41%	-9
STRUCTURAL WORK		85	06-May-26 08:00	04-Aug-26 17:00	06-May-26 08:00 A	10-Jul-26 17:00 A	37,980.00	37,980.00	37,980.00	100%	100%	22
PG-Q-CON-B-STR-10	Excavation up to bottom of footing	7	06-May-26 08:00	13-May-26 17:00	06-May-26 08:00 A	13-May-26 17:00 A	1,900.80	1,900.80	1,900.80	100%	100%	0
PG-Q-CON-B-STR-20	Anti-termite treatment and Polyethene Sheet	2	12-May-26 08:00	13-May-26 17:00	12-May-26 08:00 A	13-May-26 17:00 A	3,294.00	3,294.00	3,294.00	100%	100%	0
PG-Q-CON-B-STR-30	Backfilling with selected fill material (under footing)	1	13-May-26 08:00	13-May-26 17:00	13-May-26 08:00 A	13-May-26 17:00 A	1,900.80	1,900.80	1,900.80	100%	100%	0
PG-Q-CON-B-STR-40	Raft Foundation Work	21	13-May-26 08:00	10-Jun-26 17:00	13-May-26 08:00 A	10-Jun-26 17:00 A	2,534.40	2,534.40	2,534.40	100%	100%	0
PG-Q-CON-B-STR-50	Autoclaved aerated panel (walls)	4	25-Jul-26 08:00	28-Jul-26 17:00	08-Jul-26 08:00 A	09-Jul-26 17:00 A	11,340.00	11,340.00	11,340.00	100%	100%	2
PG-Q-CON-B-STR-60	Autoclaved aerated panel (ceiling)	3	29-Jul-26 08:00	01-Aug-26 17:00	09-Jul-26 08:00 A	10-Jul-26 17:00 A	8,505.00	8,505.00	8,505.00	100%	100%	2
PG-Q-CON-B-STR-70	Autoclaved aerated panel (parapet)	3	02-Aug-26 08:00	04-Aug-26 17:00	09-Jul-26 08:00 A	10-Jul-26 17:00 A	8,505.00	8,505.00	8,505.00	100%	100%	2
ARCHITECTURAL WORK		107	05-Aug-26 08:00	19-Oct-26 17:00	12-Jul-26 08:00 A	29-Oct-26 17:00	189,137.58	176,434.56	189,137.58	100%	93.28%	-30
GENERAL FINISHES		107	05-Aug-26 08:00	19-Oct-26 17:00	12-Jul-26 08:00 A	29-Oct-26 17:00	84,120.00	77,872.38	84,120.00	100%	92.57%	-30
PG-Q-CON-B-AR-GF-10	Block Works	6	05-Aug-26 08:00	11-Aug-26 17:00	12-Jul-26 08:00 A	16-Jul-26 17:00 A	2,484.00	2,484.00	2,484.00	100%	100%	1
PG-Q-CON-B-AR-GF-20	Plaster	7	12-Aug-26 08:00	19-Aug-26 17:00	22-Jul-26 08:00 A	05-Aug-26 17:00 A	4,427.40	4,427.40	4,427.40	100%	100%	-6
PG-Q-CON-B-AR-GF-30	False Ceiling Installation & Finishing	7	20-Aug-26 08:00	27-Aug-26 17:00	20-Aug-26 08:00 A	10-Sep-26 08:48 A	873.60	873.60	873.60	100%	100%	-11
PG-Q-CON-B-AR-GF-40	Wall Paint	12	16-Sep-26 08:00	30-Sep-26 17:00	20-Aug-26 08:00 A	06-Sep-26 12:24 A	2,958.00	2,958.00	2,958.00	100%	100%	-3
PG-Q-CON-B-AR-GF-50	Epoxy Flooring	6	01-Oct-26 08:00	07-Oct-26 17:00	20-Aug-26 08:00 A	23-Sep-26 15:24 A	273.60	273.60	273.60	100%	100%	-23
PG-Q-CON-B-AR-GF-60	Install Doors & Windows	5	08-Oct-26 08:00	13-Oct-26 17:00	27-Aug-26 08:00 A	27-Oct-26 12:48	13,273.80	9,291.66	13,273.80	100%	70%	-47
PG-Q-CON-B-AR-GF-70	Lockers and Furniture Installation	5	14-Oct-26 08:00	19-Oct-26 17:00	19-Sep-26 08:00 A	29-Oct-26 17:00	7,551.60	5,286.12	7,551.60	100%	70%	-30
PG-Q-CON-B-AR-GF-80	Facade Finishing Work	8	01-Oct-26 08:00	10-Oct-26 17:00	20-Aug-26 08:00 A	10-Sep-26 16:12 A	52,278.00	52,278.00	52,278.00	100%	100%	-11
WET AREA FINISHES		59	20-Aug-26 08:00	14-Oct-26 17:00	06-Aug-26 08:00 A	27-Oct-26 12:48	81,123.78	79,515.30	81,123.78	100%	98.02%	-23
PG-Q-CON-B-AR-WF-10	False Ceiling Installation & Finishing	7	20-Aug-26 08:00	27-Aug-26 17:00	27-Aug-26 08:00 A	04-Sep-26 08:24 A	2,898.00	2,898.00	2,898.00	100%	100%	0
PG-Q-CON-B-AR-WF-20	Wall Tiles and Partition Work	6	16-Sep-26 08:00	22-Sep-26 17:00	06-Aug-26 08:00 A	14-Aug-26 17:00 A	21,283.20	21,283.20	21,283.20	100%	100%	-1
PG-Q-CON-B-AR-WF-30	Waterproofing on Floor	6	24-Sep-26 08:00	30-Sep-26 17:00	14-Aug-26 08:00 A	07-Sep-26 15:00 A	5,784.00	5,784.00	5,784.00	100%	100%	-15
PG-Q-CON-B-AR-WF-40	Floor Tiles Works	6	01-Oct-26 08:00	07-Oct-26 17:00	14-Aug-26 08:00 A	07-Sep-26 15:00 A	6,489.00	6,489.00	6,489.00	100%	100%	-15
PG-Q-CON-B-AR-WF-50	Toilet accessories Installation Works	6	08-Oct-26 08:00	14-Oct-26 17:00	27-Aug-26 08:00 A	10-Sep-26 10:00 A	39,307.98	39,307.98	39,307.98	100%	100%	-6
PG-Q-CON-B-AR-WF-60	Install Doors	5	08-Oct-26 08:00	13-Oct-26 17:00	01-Oct-26 12:00 A	27-Oct-26 12:48	5,361.60	3,753.12	5,361.60	100%	70%	-17
ROOF FINISHES		14	01-Oct-26 08:00	19-Oct-26 17:00	20-Aug-26 08:00 A	29-Oct-26 17:00	23,893.80	19,046.88	23,893.80	100%	79.71%	-44
PG-Q-CON-B-AR-RF-10	Waterproofing on Floor	4	01-Oct-26 08:00	05-Oct-26 17:00	20-Aug-26 08:00 A	08-Sep-26 15:00 A	4,158.00	4,158.00	4,158.00	100%	100%	-13
PG-Q-CON-B-AR-RF-20	Epoxy Flooring and Finishes	6	06-Oct-26 08:00	12-Oct-26 17:00	20-Aug-26 08:00 A	26-Oct-26 14:36	10,158.00	9,142.20	10,158.00	100%	90%	-51
PG-Q-CON-B-AR-RF-30	Steel ladder and Steel roof scupper Installation	1	19-Oct-26 08:00	19-Oct-26 17:00	14-Oct-26 08:00 A	29-Oct-26 17:00	9,577.80	5,746.68	9,577.80	100%	60%	-13
MEP WORK		132	16-Jun-26 08:00	20-Oct-26 17:00	16-Jun-26 08:00 A	31-Oct-26 10:24	97,726.80	94,412.77	97,726.80	100%	96.61%	-8
MECANICAL WORKS		132	16-Jun-26 08:00	20-Oct-26 17:00	16-Jun-26 08:00 A	31-Oct-26 10:24	79,479.48	76,165.45	79,479.48	100%	95.83%	-8
FIRE FIGHTING SYSTEM		1	20-Oct-26 08:00	20-Oct-26 17:00	01-Oct-26 08:00 A	31-Oct-26 10:24	136.26	95.38	136.26	100%	70%	-24
PG-Q-CON-B-GF-FF-10	Fire Extinguisher Installation	1	20-Oct-26 08:00	20-Oct-26 17:00	01-Oct-26 08:00 A	31-Oct-26 10:24	136.26	95.38	136.26	100%	70%	-24
SEWER AND DRAINAGE SYSTEM		103	16-Jun-26 08:00	02-Sep-26 17:00	16-Jun-26 08:00 A	26-Oct-26 08:48	11,290.02	10,322.30	11,290.02	100%	91.43%	-44
PG-Q-CON-B-GF-DR-10	Sewer and Drainge System Main Lines Installation	2	16-Jun-26 08:00	17-Jun-26 17:00	16-Jun-26 08:00 A	17-Jun-26 17:00 A	3,225.72	3,225.72	3,225.72	100%	100%	0
PG-Q-CON-B-GF-DR-20	Sewer and Drainge System Pipes and fittings Installation	2	16-Jun-26 08:00	17-Jun-26 17:00	16-Jun-26 08:00 A	17-Jun-26 17:00 A	4,838.58	4,838.58	4,838.58	100%	100%	0
PG-Q-CON-B-GF-DR-30	Sanitaryware Installation (Final Fix)	2	01-Sep-26 08:00	02-Sep-26 17:00	01-Oct-26 08:00 A	26-Oct-26 08:48	3,225.72	2,258.00	3,225.72	100%	70%	-19
HVAC SYSTEM		26	12-Aug-26 08:00	23-Aug-26 17:00	13-Aug-26 08:00 A	24-Oct-26 16:12	12,127.20	9,821.76	12,127.20	100%	80.99%	-51
PG-Q-CON-B-GF-AC-10	Duct Work and Exhaust Fan Installation	7	12-Aug-26 08:00	19-Aug-26 17:00	13-Aug-26 08:00 A	20-Aug-26 17:00 A	4,442.40	4,442.40	4,442.40	100%	100%	0
PG-Q-CON-B-GF-AC-20	Split AC, Grills & Diffuser Installation	3	20-Aug-26 08:00	23-Aug-26 17:00	01-Oct-26 08:00 A	24-Oct-26 16:12	7,684.80	5,379.36	7,684.80	100%	70%	-17
WATER SUPPLY SYSTEM		80	16-Jun-26 08:00	31-Aug-26 17:00	16-Jun-26 08:00 A	07-Sep-26 10:24 A	55,926.00	55,926.00	55,926.00	100%	100%	-5
PG-Q-CON-B-GF-WS-10	Water Supply Main Lines Installation	2	16-Jun-26 08:00	17-Jun-26 17:00	16-Jun-26 08:00 A	17-Jun-26 17:00 A	5,702.40	5,702.40	5,702.40	100%	100%	0
PG-Q-CON-B-GF-WS-20	Water Supply Pipes Installation (Cold and Hot Water)	2	24-Aug-26 08:00	25-Aug-26 17:00	22-Jul-26 08:00 A	31-Jul-26 17:00 A	13,857.60	13,857.60	13,857.60	100%	100%	-6
PG-Q-CON-B-GF-WS-30	Water Supply Accesories and Booster pump Installation	3	29-Aug-26 08:00	31-Aug-26 17:00	20-Aug-26 08:00 A	07-Sep-26 10:24 A	36,366.00	36,366.00	36,366.00	100%	100%	-12
ELECTRICAL WORKS		47	13-Jul-26 08:00	15-Sep-26 17:00	22-Jul-26 08:00 A	08-Sep-26 15:24 A	18,247.32	18,247.32	18,247.32	100%	100%	14
PG-Q-CON-B-GF-EL-10	Pipes & Conduits Installation	8	13-Jul-26 08:00	21-Jul-26 17:00	22-Jul-26 08:00 A	23-Jul-26 17:00 A	1,983.60	1,983.60	1,983.60	100%	100%	6
PG-Q-CON-B-GF-EL-20	Electrical & ELV Wiring Works	3	13-Sep-26 08:00	15-Sep-26 17:00	20-Aug-26 08:00 A	08-Sep-26 15:24 A	1,983.60	1,983.60	1,983.60	100%	100%	-14
PG-Q-CON-B-GF-EL-30	Fire Alarm Devices Installation	3	06-Sep-26 08:00	08-Sep-26 17:00	20-Aug-26 08:00 A	08-Sep-26 15:24 A	1,983.60	1,983.60	1,983.60	100%	100%	-14
PG-Q-CON-B-GF-EL-40	Telecom & CCTV Devices Installation	3	09-Sep-26 08:00	12-Sep-26 17:00	20-Aug-26 08:00 A	08-Sep-26 15:24 A	4,959.00	4,959.00	4,959.00	100%	100%	-14
PG-Q-CON-B-GF-EL-50	Electrical Light Fixtures Installation	2	03-Sep-26 08:00	05-Sep-26 17:00	20-Aug-26 08:00 A	08-Sep-26 15:24 A	7,337.52	7,337.52	7,337.52	100%	100%	-15
PROJECT CLOSOUT		225	23-May-26 08:00	16-Dec-26 17:00	22-May-26 09:36 A	14-Feb-27 15:24	52,612.62	324,444.49	1,753,754.00	3%	18.5%	-51
PG-Q-PCL-10	Testing, Commissioning for All Systems(Completed)	25	23-May-26 08:00	24-Jun-26 17:00	22-May-26 09:36 A	24-Jun-26 17:00 A	52,612.62	52,612.62	52,612.62	100%	100%	0
PG-Q-PCL-10_R	Testing, Commissioning for All Systems(Remaining)	11	16-Nov-26 08:00	26-Nov-26 17:00	06-Aug-26 08:00 A	25-Jan-27 15:24	0.00	236,756.79	473,513.58	0%	50%	-137
PG-Q-PCL-20	As-Built Drawings	15	16-Nov-26 08:00	02-Dec-26 17:00	23-Sep-26 11:41 A	02-Feb-27 11:12	0.00	35,075.08	175,375.40	0%	20%	-97
PG-Q-PCL-30	Snag list Submission	3	28-Nov-26 08:00	30-Nov-26 17:00	25-Jan-27 15:24	28-Jan-27 15:24	0.00	0.00	350,750.80	0%	0%	0
PG-Q-PCL-40	Snag list Closeout	10	01-Dec-26 08:00	12-Dec-26 17:00	28-Jan-27 15:24	09-Feb-27 15:24	0.00	0.00	350,750.80	0%	0%	0
PG-Q-PCL-50	Issuing Approvals	3	13-Dec-26 08:00	15-Dec-26 17:00	09-Feb-27 15:24	13-Feb-27 15:24	0.00	0.00	175,375.40	0%	0%	0
PG-Q-PCL-60	Handing Over	1	16-Dec-26 08:00	16-Dec-26 17:00	13-Feb-27 15:24	14-Feb-27 15:24	0.00	0.00	175,375.40	0%	0%	0
HAIL		272	17-Feb-26 08:00	15-Dec-26 17:00	17-Feb-26 08:00 A	09-Jan-27 12:48	6,006,753.31	5,675,326.67	6,814,652.00	88.14%	83.28%	-21
MOBILIZATION		29	17-Feb-26 08:00	29-Mar-26 10:00	17-Feb-26 08:00 A	28-Mar-26 17:00 A	0.00	0.00	0.00	0%	0%	0
TEMPORARY CAMP		28	17-Feb-26 08:00	28-Mar-26 09:00	17-Feb-26 08:00 A	27-Mar-26 17:00 A	0.00	0.00	0.00	0%	0%	0
PG-HMOB-CAM-10	Temporary Underground Utilities works	28	17-Feb-26 08:00	28-Mar-26 09:00	17-Feb-26 08:00 A	27-Mar-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-HMOB-CAM-20	Temporary Porta-Cabins	21	26-Feb-26 08:00	28-Mar-26 09:00	26-Feb-26 08:00 A	27-Mar-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-HMOB-CAM-30	Temporary Toilets	21	26-Feb-26 08:00	28-Mar-26 09:00	26-Feb-26 08:00 A	27-Mar-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-HMOB-CAM-40	Temporary Mosque	13	08-Mar-26 08:00	28-Mar-26 09:00	08-Mar-26 08:00 A	27-Mar-26 17:00 A	0.00	0.00	0.00	100%	100%	0
SITE OFFICES		29	17-Feb-26 08:00	29-Mar-26 10:00	17-Feb-26 08:00 A	28-Mar-26 17:00 A	0.00	0.00	0.00	0%	0%	0
PG-HMOB-SO-10	Temporary Underground Utilities works	29	17-Feb-26 08:00	29-Mar-26 10:00	17-Feb-26 08:00 A	28-Mar-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-HMOB-SO-20	Temporary Porta-Cabins	23	25-Feb-26 08:00	29-Mar-26 10:00	25-Feb-26 08:00 A	28-Mar-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-HMOB-SO-30	Temporary Toilets	23	25-Feb-26 08:00	29-Mar-26 10:00	25-Feb-26 08:00 A	28-Mar-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-HMOB-SO-40	Temporary Mosque	17	04-Mar-26 08:00	29-Mar-26 10:00	04-Mar-26 08:00 A	28-Mar-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-HMOB-SO-50	Car Parking Area	10	12-Mar-26 08:00	29-Mar-26 10:00	12-Mar-26 08:00 A	28-Mar-26 17:00 A	0.00	0.00	0.00	100%	100%	0
GENERAL REQUIEREMENTS		51	17-Feb-26 08:00	23-Apr-26 10:00	17-Feb-26 08:00 A	22-Apr-26 17:00 A	0.00	0.00	0.00	0%	0%	0




Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining W...
Milestone
summary

Baseline Schedule Rev.00

PLAYGROUNDS INITIATIVE - QASSIM, HAIL & TABUK - 25-Oct-2026

Activity ID	Activity Name	O.D	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Schedule % Complete	Performance % Complete	Variance - BL Project Duration
PG-H-GEN-10	QA/QC Submission Plan	16	12-Mar-26 08:00	05-Apr-26 10:00	12-Mar-26 08:00 A	04-Apr-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-H-GEN-20	HSSE Submission Plan	51	17-Feb-26 08:00	23-Apr-26 10:00	17-Feb-26 08:00 A	22-Apr-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-H-GEN-30	Surveying report Submission Plan	51	17-Feb-26 08:00	23-Apr-26 10:00	17-Feb-26 08:00 A	22-Apr-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-H-GEN-40	Baseline Submission	6	28-Feb-26 08:00	07-Mar-26 10:00	28-Feb-26 08:00 A	05-Mar-26 17:00 A	0.00	0.00	0.00	100%	100%	0
ENGINEERING		168	17-Feb-26 08:00	14-Jul-26 17:00	17-Feb-26 08:00 A	17-Sep-26 17:00 A	204,439.56	204,439.56	204,439.56	100%	100%	-56
SHOP DRAWINGS SUBMITTALS		93	17-Feb-26 08:00	16-Jun-26 10:00	17-Feb-26 08:00 A	15-Jun-26 17:00 A	0.00	0.00	0.00	0%	0%	0
STRUCTURAL DRAWINGS		61	17-Feb-26 08:00	05-May-26 10:00	17-Feb-26 08:00 A	04-May-26 17:00 A	0.00	0.00	0.00	0%	0%	0
PROJECT FENCE		57	17-Feb-26 08:00	30-Apr-26 10:00	17-Feb-26 08:00 A	29-Apr-26 17:00 A	0.00	0.00	0.00	0%	0%	0
PG-H-EN-ST-SD-SB-10	Excavation Drawings	57	17-Feb-26 08:00	30-Apr-26 10:00	17-Feb-26 08:00 A	29-Apr-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-H-EN-ST-SD-SB-20	Foundation Drawings	55	19-Feb-26 08:00	30-Apr-26 10:00	19-Feb-26 08:00 A	29-Apr-26 17:00 A	0.00	0.00	0.00	100%	100%	0
TOILET BUILDING		41	19-Feb-26 08:00	14-Apr-26 10:00	19-Feb-26 08:00 A	13-Apr-26 17:00 A	0.00	0.00	0.00	0%	0%	0
PG-H-EN-ST-SD-SB-30	Excavation Drawings	41	19-Feb-26 08:00	14-Apr-26 10:00	19-Feb-26 08:00 A	13-Apr-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-H-EN-ST-SD-SB-40	Foundation Drawings	39	23-Feb-26 08:00	14-Apr-26 10:00	23-Feb-26 08:00 A	13-Apr-26 17:00 A	0.00	0.00	0.00	100%	100%	0
WATER STORAGE TANK		39	23-Feb-26 08:00	14-Apr-26 10:00	23-Feb-26 08:00 A	13-Apr-26 17:00 A	0.00	0.00	0.00	0%	0%	0
PG-H-EN-ST-SD-SB-50	Foundation Drawings	37	25-Feb-26 08:00	14-Apr-26 10:00	25-Feb-26 08:00 A	13-Apr-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-H-EN-ST-SD-SB-60	Excavation Drawings	39	23-Feb-26 08:00	14-Apr-26 10:00	23-Feb-26 08:00 A	13-Apr-26 17:00 A	0.00	0.00	0.00	100%	100%	0
SEPTIC TANK		55	25-Feb-26 08:00	05-May-26 10:00	25-Feb-26 08:00 A	04-May-26 17:00 A	0.00	0.00	0.00	0%	0%	0
PG-H-EN-ST-SD-SB-70	Reinforcement Detail Drawings	55	25-Feb-26 08:00	05-May-26 10:00	25-Feb-26 08:00 A	04-May-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-H-EN-ST-SD-SB-80	Concrete Detail Drawings	52	01-Mar-26 08:00	05-May-26 10:00	01-Mar-26 08:00 A	04-May-26 17:00 A	0.00	0.00	0.00	100%	100%	0
ARCHITECTURAL DRAWINGS		39	23-Feb-26 08:00	14-Apr-26 10:00	23-Feb-26 08:00 A	13-Apr-26 17:00 A	0.00	0.00	0.00	0%	0%	0
TOILET BUILDING		39	23-Feb-26 08:00	14-Apr-26 10:00	23-Feb-26 08:00 A	13-Apr-26 17:00 A	0.00	0.00	0.00	0%	0%	0
PG-H-EN-AR-SD-SB-10	Ground Floor Plan	36	23-Feb-26 08:00	11-Apr-26 10:00	23-Feb-26 08:00 A	09-Apr-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-H-EN-AR-SD-SB-100	Cladding Details	32	03-Mar-26 08:00	14-Apr-26 10:00	03-Mar-26 08:00 A	13-Apr-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-H-EN-AR-SD-SB-20	Roof Floor Plan	35	28-Feb-26 08:00	14-Apr-26 10:00	28-Feb-26 08:00 A	13-Apr-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-H-EN-AR-SD-SB-30	Elevations	29	03-Mar-26 08:00	11-Apr-26 10:00	03-Mar-26 08:00 A	09-Apr-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-H-EN-AR-SD-SB-40	Sections	27	05-Mar-26 08:00	11-Apr-26 10:00	05-Mar-26 08:00 A	09-Apr-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-H-EN-AR-SD-SB-50	Floor Finish Layout	32	28-Feb-26 08:00	09-Apr-26 13:00	28-Feb-26 08:00 A	09-Apr-26 12:00 A	0.00	0.00	0.00	100%	100%	0
PG-H-EN-AR-SD-SB-60	Reflected Ceiling Layout	32	28-Feb-26 08:00	11-Apr-26 10:00	28-Feb-26 08:00 A	09-Apr-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-H-EN-AR-SD-SB-70	Enlarged Toilets Layout	35	28-Feb-26 08:00	14-Apr-26 10:00	28-Feb-26 08:00 A	13-Apr-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-H-EN-AR-SD-SB-80	Doors & Windows Schedule	32	03-Mar-26 08:00	14-Apr-26 10:00	03-Mar-26 08:00 A	13-Apr-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-H-EN-AR-SD-SB-90	Aluminum Work	32	03-Mar-26 08:00	14-Apr-26 10:00	03-Mar-26 08:00 A	13-Apr-26 17:00 A	0.00	0.00	0.00	100%	100%	0
LANDSCAPE DRAWINGS		38	24-Feb-26 08:00	14-Apr-26 10:00	24-Feb-26 08:00 A	13-Apr-26 17:00 A	0.00	0.00	0.00	0%	0%	0
PG-H-EN-LS-SD-SB-10	Hardscape Layout Plan	38	24-Feb-26 08:00	14-Apr-26 10:00	24-Feb-26 08:00 A	13-Apr-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-H-EN-LS-SD-SB-100	Playground Details	35	24-Feb-26 08:00	11-Apr-26 10:00	24-Feb-26 08:00 A	09-Apr-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-H-EN-LS-SD-SB-20	Interlock Tile Details	35	24-Feb-26 08:00	11-Apr-26 10:00	24-Feb-26 08:00 A	09-Apr-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-H-EN-LS-SD-SB-30	Stamped Concrete Pattern & Section	38	24-Feb-26 08:00	14-Apr-26 10:00	24-Feb-26 08:00 A	13-Apr-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-H-EN-LS-SD-SB-40	Tartan Flooring Layout & Details	38	24-Feb-26 08:00	14-Apr-26 10:00	24-Feb-26 08:00 A	13-Apr-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-H-EN-LS-SD-SB-50	Bike Path Layout & Details	35	24-Feb-26 08:00	11-Apr-26 10:00	24-Feb-26 08:00 A	09-Apr-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-H-EN-LS-SD-SB-60	Walking Path layout & Details	35	24-Feb-26 08:00	11-Apr-26 10:00	24-Feb-26 08:00 A	09-Apr-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-H-EN-LS-SD-SB-70	Tree Planting Plan & Details	35	24-Feb-26 08:00	11-Apr-26 10:00	24-Feb-26 08:00 A	09-Apr-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-H-EN-LS-SD-SB-80	Traffic Sign Location & Details	38	24-Feb-26 08:00	14-Apr-26 10:00	24-Feb-26 08:00 A	13-Apr-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-H-EN-LS-SD-SB-90	Football Playground Layout	38	24-Feb-26 08:00	14-Apr-26 10:00	24-Feb-26 08:00 A	13-Apr-26 17:00 A	0.00	0.00	0.00	100%	100%	0
MECHANICAL DRAWINGS		52	01-Mar-26 08:00	05-May-26 10:00	01-Mar-26 08:00 A	04-May-26 17:00 A	0.00	0.00	0.00	0%	0%	0
WATER SUPPLY SYSTEM		31	01-Mar-26 08:00	11-Apr-26 10:00	01-Mar-26 08:00 A	09-Apr-26 17:00 A	0.00	0.00	0.00	0%	0%	0
PG-H-EN-ME-SD-SB-10	Cold & Hot Water Piping Layout	27	05-Mar-26 08:00	11-Apr-26 10:00	05-Mar-26 08:00 A	09-Apr-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-H-EN-ME-SD-SB-20	Pump Room Layout	31	01-Mar-26 08:00	11-Apr-26 10:00	01-Mar-26 08:00 A	09-Apr-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-H-EN-ME-SD-SB-30	Booster Pump Details	27	05-Mar-26 08:00	11-Apr-26 10:00	05-Mar-26 08:00 A	09-Apr-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-H-EN-ME-SD-SB-40	GRP Water Tank Details	23	10-Mar-26 08:00	11-Apr-26 10:00	10-Mar-26 08:00 A	09-Apr-26 17:00 A	0.00	0.00	0.00	100%	100%	0
SEWER AND DRAINAGE SYSTEM		27	05-Mar-26 08:00	11-Apr-26 10:00	05-Mar-26 08:00 A	09-Apr-26 17:00 A	0.00	0.00	0.00	0%	0%	0
PG-H-EN-ME-SD-SB-50	Drainage Layout	27	05-Mar-26 08:00	11-Apr-26 10:00	05-Mar-26 08:00 A	09-Apr-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-H-EN-ME-SD-SB-60	Floor Drains & Cleanouts Details	23	10-Mar-26 08:00	11-Apr-26 10:00	10-Mar-26 08:00 A	09-Apr-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-H-EN-ME-SD-SB-70	Inspection Chamber Details	20	14-Mar-26 08:00	11-Apr-26 10:00	14-Mar-26 08:00 A	09-Apr-26 17:00 A	0.00	0.00	0.00	100%	100%	0
IRRIGATION SYSTEM		44	10-Mar-26 08:00	05-May-26 10:00	10-Mar-26 08:00 A	04-May-26 17:00 A	0.00	0.00	0.00	0%	0%	0
PG-H-EN-ME-SD-SB-80	HDPE Pipe Routing	44	10-Mar-26 08:00	05-May-26 10:00	10-Mar-26 08:00 A	04-May-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-H-EN-ME-SD-SB-90	Irrigation Network Layout	41	14-Mar-26 08:00	05-May-26 10:00	14-Mar-26 08:00 A	04-May-26 17:00 A	0.00	0.00	0.00	100%	100%	0
ELECTRICAL DRAWINGS		27	11-May-26 08:00	16-Jun-26 10:00	11-May-26 08:00 A	15-Jun-26 17:00 A	0.00	0.00	0.00	0%	0%	0
POWER AND LIGHTING SYSTEM		27	11-May-26 08:00	16-Jun-26 10:00	11-May-26 08:00 A	15-Jun-26 17:00 A	0.00	0.00	0.00	0%	0%	0
PG-H-EN-EL-SD-SB-10	Main Distribution Board (MDB) Layout	27	11-May-26 08:00	16-Jun-26 10:00	11-May-26 08:00 A	15-Jun-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-H-EN-EL-SD-SB-20	Pump Room Power Panel	27	11-May-26 08:00	16-Jun-26 10:00	11-May-26 08:00 A	15-Jun-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-H-EN-EL-SD-SB-30	Street Lighting Power Panel	27	11-May-26 08:00	16-Jun-26 10:00	11-May-26 08:00 A	15-Jun-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-H-EN-EL-SD-SB-40	Site Lighting Pole Layout	27	11-May-26 08:00	16-Jun-26 10:00	11-May-26 08:00 A	15-Jun-26 17:00 A	0.00	0.00	0.00	100%	100%	0
ELV SYSTEM		27	11-May-26 08:00	16-Jun-26 10:00	11-May-26 08:00 A	15-Jun-26 17:00 A	0.00	0.00	0.00	0%	0%	0
PG-H-EN-EL-SD-SB-50	Telecom & Data Layout	27	11-May-26 08:00	16-Jun-26 10:00	11-May-26 08:00 A	15-Jun-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-H-EN-EL-SD-SB-60	CCTV Camera Layout	27	11-May-26 08:00	16-Jun-26 10:00	11-May-26 08:00 A	15-Jun-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-H-EN-EL-SD-SB-70	Access Control Layout	27	11-May-26 08:00	16-Jun-26 10:00	11-May-26 08:00 A	15-Jun-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-H-EN-EL-SD-SB-80	AV System Layout	27	11-May-26 08:00	16-Jun-26 10:00	11-May-26 08:00 A	15-Jun-26 17:00 A	0.00	0.00	0.00	100%	100%	0
FIRE ALARM SYSTEM		27	11-May-26 08:00	16-Jun-26 10:00	11-May-26 08:00 A	15-Jun-26 17:00 A	0.00	0.00	0.00	0%	0%	0
PG-H-EN-EL-SD-SB-100	Detector & Manual Call Point Details	27	11-May-26 08:00	16-Jun-26 10:00	11-May-26 08:00 A	15-Jun-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-H-EN-EL-SD-SB-110	Control Panel Wiring Diagram	27	11-May-26 08:00	16-Jun-26 10:00	11-May-26 08:00 A	15-Jun-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-H-EN-EL-SD-SB-90	Fire Alarm Layout	27	11-May-26 08:00	16-Jun-26 10:00	11-May-26 08:00 A	15-Jun-26 17:00 A	0.00	0.00	0.00	100%	100%	0
SHOP DRAWINGS APPROVALS		92	19-Feb-26 08:00	17-Jun-26 10:00	19-Feb-26 08:00 A	16-Jun-26 17:00 A	0.00	0.00	0.00	0%	0%	0
STRUCTURAL DRAWINGS		61	19-Feb-26 08:00	07-May-26 10:00	19-Feb-26 08:00 A	06-May-26 17:00 A	0.00	0.00	0.00	0%	0%	0
PROJECT FENCE		55	19-Feb-26 08:00	30-Apr-26 10:00	19-Feb-26 08:00 A	29-Apr-26 17:00 A	0.00	0.00	0.00	0%	0%	0

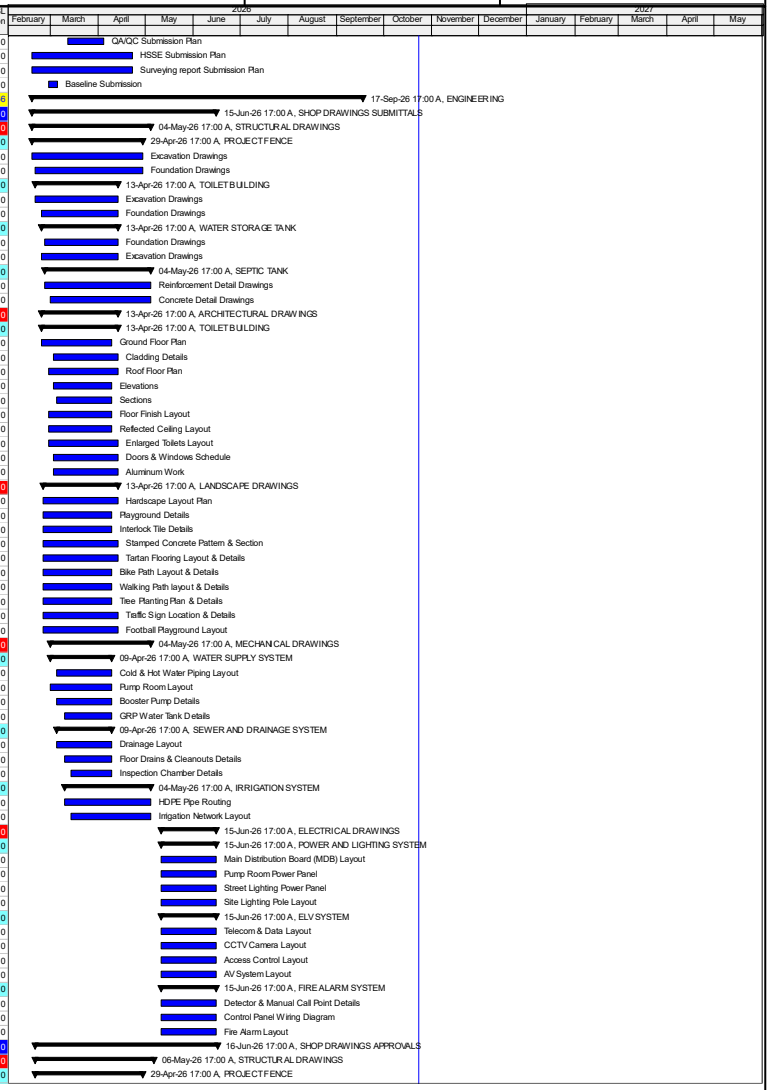


Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining W...
Milestone
summary

Baseline Schedule Rev.00

PLAYGROUNDS INITIATIVE - QASSIM, HAIL & TABUK - 25-Oct-2026

Activity ID	Activity Name	O.D	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Schedule % Complete	Performance % Complete	Variance - BL Project Duration
PG-H-EN-ST-SD-AP-10	Excavation Drawings	55	19-Feb-26 08:00	30-Apr-26 10:00	19-Feb-26 08:00 A	29-Apr-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-H-EN-ST-SD-AP-20	Foundation Drawings	52	24-Feb-26 08:00	30-Apr-26 10:00	24-Feb-26 08:00 A	29-Apr-26 17:00 A	0.00	0.00	0.00	100%	100%	0
TOILET BUILDING		42	23-Feb-26 08:00	18-Apr-26 10:00	23-Feb-26 08:00 A	16-Apr-26 17:00 A	0.00	0.00	0.00	0%	0%	0
PG-H-EN-ST-SD-AP-30	Excavation Drawings	42	23-Feb-26 08:00	18-Apr-26 10:00	23-Feb-26 08:00 A	16-Apr-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-H-EN-ST-SD-AP-40	Foundation Drawings	39	26-Feb-26 08:00	18-Apr-26 10:00	26-Feb-26 08:00 A	16-Apr-26 17:00 A	0.00	0.00	0.00	100%	100%	0
WATER STORAGE TANK		40	25-Feb-26 08:00	18-Apr-26 10:00	25-Feb-26 08:00 A	16-Apr-26 17:00 A	0.00	0.00	0.00	0%	0%	0
PG-H-EN-ST-SD-AP-50	Excavation Drawings	40	25-Feb-26 08:00	18-Apr-26 10:00	25-Feb-26 08:00 A	16-Apr-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-H-EN-ST-SD-AP-60	Foundation Drawings	37	01-Mar-26 08:00	18-Apr-26 10:00	01-Mar-26 08:00 A	16-Apr-26 17:00 A	0.00	0.00	0.00	100%	100%	0
SEPTIC TANK		54	01-Mar-26 08:00	07-May-26 10:00	01-Mar-26 08:00 A	06-May-26 17:00 A	0.00	0.00	0.00	0%	0%	0
PG-H-EN-ST-SD-AP-70	Reinforcement Detail Drawings	54	01-Mar-26 08:00	07-May-26 10:00	01-Mar-26 08:00 A	06-May-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-H-EN-ST-SD-AP-80	Concrete Detail Drawings	51	04-Mar-26 08:00	07-May-26 10:00	04-Mar-26 08:00 A	06-May-26 17:00 A	0.00	0.00	0.00	100%	100%	0
ARCHITECTURAL DRAWINGS		38	28-Feb-26 08:00	18-Apr-26 10:00	28-Feb-26 08:00 A	16-Apr-26 17:00 A	0.00	0.00	0.00	0%	0%	0
TOILET BUILDING		38	28-Feb-26 08:00	18-Apr-26 10:00	28-Feb-26 08:00 A	16-Apr-26 17:00 A	0.00	0.00	0.00	0%	0%	0
PG-H-EN-AR-SD-AP-10	Ground Floor Plan	38	28-Feb-26 08:00	18-Apr-26 10:00	28-Feb-26 08:00 A	16-Apr-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-H-EN-AR-SD-AP-100	Cladding Details	31	08-Mar-26 08:00	18-Apr-26 10:00	08-Mar-26 08:00 A	16-Apr-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-H-EN-AR-SD-AP-20	Roof Floor Plan	35	03-Mar-26 08:00	18-Apr-26 10:00	03-Mar-26 08:00 A	16-Apr-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-H-EN-AR-SD-AP-30	Elevations	32	07-Mar-26 08:00	18-Apr-26 10:00	07-Mar-26 08:00 A	16-Apr-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-H-EN-AR-SD-AP-40	Sections	29	10-Mar-26 08:00	18-Apr-26 10:00	10-Mar-26 08:00 A	16-Apr-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-H-EN-AR-SD-AP-50	Floor Finish Layout	33	05-Mar-26 08:00	18-Apr-26 10:00	05-Mar-26 08:00 A	16-Apr-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-H-EN-AR-SD-AP-60	Reflected Ceiling Layout	33	05-Mar-26 08:00	18-Apr-26 10:00	05-Mar-26 08:00 A	16-Apr-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-H-EN-AR-SD-AP-70	Enlarged Toilets Layout	33	05-Mar-26 08:00	18-Apr-26 10:00	05-Mar-26 08:00 A	16-Apr-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-H-EN-AR-SD-AP-80	Doors & Windows Schedule	32	07-Mar-26 08:00	18-Apr-26 10:00	07-Mar-26 08:00 A	16-Apr-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-H-EN-AR-SD-AP-90	Aluminum Work	31	08-Mar-26 08:00	18-Apr-26 10:00	08-Mar-26 08:00 A	16-Apr-26 17:00 A	0.00	0.00	0.00	100%	100%	0
LANDSCAPE DRAWINGS		38	28-Feb-26 08:00	18-Apr-26 10:00	28-Feb-26 08:00 A	16-Apr-26 17:00 A	0.00	0.00	0.00	0%	0%	0
PG-H-EN-LS-SD-AP-10	Hardscape Layout Plan	37	01-Mar-26 08:00	18-Apr-26 10:00	01-Mar-26 08:00 A	16-Apr-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-H-EN-LS-SD-AP-100	Playground Details	37	01-Mar-26 08:00	18-Apr-26 10:00	01-Mar-26 08:00 A	16-Apr-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-H-EN-LS-SD-AP-20	Interlock Tile Details	29	10-Mar-26 08:00	18-Apr-26 10:00	10-Mar-26 08:00 A	16-Apr-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-H-EN-LS-SD-AP-30	Stamped Concrete Pattern & Section	23	17-Mar-26 08:00	18-Apr-26 10:00	17-Mar-26 08:00 A	16-Apr-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-H-EN-LS-SD-AP-40	Tartan Flooring Layout & Details	37	01-Mar-26 08:00	18-Apr-26 10:00	01-Mar-26 08:00 A	16-Apr-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-H-EN-LS-SD-AP-50	Bike Path Layout & Details	38	28-Feb-26 08:00	18-Apr-26 10:00	28-Feb-26 08:00 A	16-Apr-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-H-EN-LS-SD-AP-60	Walking Path layout & Details	38	28-Feb-26 08:00	18-Apr-26 10:00	28-Feb-26 08:00 A	16-Apr-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-H-EN-LS-SD-AP-70	Tee Planting Plan & Details	37	01-Mar-26 08:00	18-Apr-26 10:00	01-Mar-26 08:00 A	16-Apr-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-H-EN-LS-SD-AP-80	Traffic Sign Location & Details	38	28-Feb-26 08:00	18-Apr-26 10:00	28-Feb-26 08:00 A	16-Apr-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-H-EN-LS-SD-AP-90	Football Playground Layout	37	01-Mar-26 08:00	18-Apr-26 10:00	01-Mar-26 08:00 A	16-Apr-26 17:00 A	0.00	0.00	0.00	100%	100%	0
MECHANICAL DRAWINGS		46	10-Mar-26 08:00	07-May-26 10:00	10-Mar-26 08:00 A	06-May-26 17:00 A	0.00	0.00	0.00	0%	0%	0
WATER SUPPLY SYSTEM		26	10-Mar-26 08:00	14-Apr-26 10:00	10-Mar-26 08:00 A	13-Apr-26 17:00 A	0.00	0.00	0.00	0%	0%	0
PG-H-EN-ME-SD-AP-10	Cold & Hot Water Piping Layout	26	10-Mar-26 08:00	14-Apr-26 10:00	10-Mar-26 08:00 A	13-Apr-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-H-EN-ME-SD-AP-20	Pump Room Layout	20	17-Mar-26 08:00	14-Apr-26 10:00	17-Mar-26 08:00 A	13-Apr-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-H-EN-ME-SD-AP-30	Booster Pump Details	25	11-Mar-26 08:00	14-Apr-26 10:00	11-Mar-26 08:00 A	13-Apr-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-H-EN-ME-SD-AP-40	GRP Water Tank Details	22	15-Mar-26 08:00	14-Apr-26 10:00	15-Mar-26 08:00 A	13-Apr-26 17:00 A	0.00	0.00	0.00	100%	100%	0
SEWER AND DRAINAGE SYSTEM		26	10-Mar-26 08:00	14-Apr-26 10:00	10-Mar-26 08:00 A	13-Apr-26 17:00 A	0.00	0.00	0.00	0%	0%	0
PG-H-EN-ME-SD-AP-50	Drainage Layout	26	10-Mar-26 08:00	14-Apr-26 10:00	10-Mar-26 08:00 A	13-Apr-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-H-EN-ME-SD-AP-60	Floor Drains & Cleanouts Details	20	17-Mar-26 08:00	14-Apr-26 10:00	17-Mar-26 08:00 A	13-Apr-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-H-EN-ME-SD-AP-70	Inspection Chamber Details	20	17-Mar-26 08:00	14-Apr-26 10:00	17-Mar-26 08:00 A	13-Apr-26 17:00 A	0.00	0.00	0.00	100%	100%	0
IRRIGATION SYSTEM		43	14-Mar-26 08:00	07-May-26 10:00	14-Mar-26 08:00 A	06-May-26 17:00 A	0.00	0.00	0.00	0%	0%	0
PG-H-EN-ME-SD-AP-80	HDPE Pipe Routing	43	14-Mar-26 08:00	07-May-26 10:00	14-Mar-26 08:00 A	06-May-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-H-EN-ME-SD-AP-90	Irrigation Network Layout	39	18-Mar-26 08:00	07-May-26 10:00	18-Mar-26 08:00 A	06-May-26 17:00 A	0.00	0.00	0.00	100%	100%	0
ELECTRICAL DRAWINGS		27	12-May-26 08:00	17-Jun-26 10:00	12-May-26 08:00 A	16-Jun-26 17:00 A	0.00	0.00	0.00	0%	0%	0
POWER AND LIGHTING SYSTEM		27	12-May-26 08:00	17-Jun-26 10:00	12-May-26 08:00 A	16-Jun-26 17:00 A	0.00	0.00	0.00	0%	0%	0
PG-H-EN-EL-SD-AP-10	Main Distribution Board (MDB) Layout	27	12-May-26 08:00	17-Jun-26 10:00	12-May-26 08:00 A	16-Jun-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-H-EN-EL-SD-AP-20	Pump Room Power Panel	27	12-May-26 08:00	17-Jun-26 10:00	12-May-26 08:00 A	16-Jun-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-H-EN-EL-SD-AP-30	Street Lighting Power Panel	27	12-May-26 08:00	17-Jun-26 10:00	12-May-26 08:00 A	16-Jun-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-H-EN-EL-SD-AP-40	Site Lighting Pole Layout	27	12-May-26 08:00	17-Jun-26 10:00	12-May-26 08:00 A	16-Jun-26 17:00 A	0.00	0.00	0.00	100%	100%	0
ELV SYSTEM		27	12-May-26 08:00	17-Jun-26 10:00	12-May-26 08:00 A	16-Jun-26 17:00 A	0.00	0.00	0.00	0%	0%	0
PG-H-EN-EL-SD-AP-50	Telecom & Data Layout	27	12-May-26 08:00	17-Jun-26 10:00	12-May-26 08:00 A	16-Jun-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-H-EN-EL-SD-AP-60	CCTV Camera Layout	27	12-May-26 08:00	17-Jun-26 10:00	12-May-26 08:00 A	16-Jun-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-H-EN-EL-SD-AP-70	Access Control Layout	27	12-May-26 08:00	17-Jun-26 10:00	12-May-26 08:00 A	16-Jun-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-H-EN-EL-SD-AP-80	AV System Layout	27	12-May-26 08:00	17-Jun-26 10:00	12-May-26 08:00 A	16-Jun-26 17:00 A	0.00	0.00	0.00	100%	100%	0
FIRE ALARM SYSTEM		27	12-May-26 08:00	17-Jun-26 10:00	12-May-26 08:00 A	16-Jun-26 17:00 A	0.00	0.00	0.00	0%	0%	0
PG-H-EN-EL-SD-AP-100	Detector & Manual Call Point Details	27	12-May-26 08:00	17-Jun-26 10:00	12-May-26 08:00 A	16-Jun-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-H-EN-EL-SD-AP-110	Control Panel Wiring Diagram	27	12-May-26 08:00	17-Jun-26 10:00	12-May-26 08:00 A	16-Jun-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-H-EN-EL-SD-AP-90	Fire Alarm Layout	27	12-May-26 08:00	17-Jun-26 10:00	12-May-26 08:00 A	16-Jun-26 17:00 A	0.00	0.00	0.00	100%	100%	0
MATERIAL SUBMITTALS		166	17-Feb-26 08:00	06-Jul-26 17:00	17-Feb-26 08:00 A	01-Sep-26 11:12 A	0.00	0.00	0.00	0%	0%	-48
LONG LEAD ITEMS		163	21-Feb-26 08:00	06-Jul-26 17:00	21-Feb-26 08:00 A	01-Sep-26 11:12 A	0.00	0.00	0.00	0%	0%	-48
EXTERNAL / LANDSCAPE WORK		56	25-Feb-26 08:00	06-May-26 10:00	25-Feb-26 08:00 A	05-May-26 17:00 A	0.00	0.00	0.00	0%	0%	0
PG-H-PR-LL-LS-MS-10	Bike and Walk Path Materials	48	07-Mar-26 08:00	06-May-26 10:00	07-Mar-26 08:00 A	05-May-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-H-PR-LL-LS-MS-20	Benches, Seats (Rectangular & Circular)	56	25-Feb-26 08:00	06-May-26 10:00	25-Feb-26 08:00 A	05-May-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-H-PR-LL-LS-MS-30	Fence, gates and accessories	56	25-Feb-26 08:00	06-May-26 10:00	25-Feb-26 08:00 A	05-May-26 17:00 A	0.00	0.00	0.00	100%	100%	0
SPORTS & RECREATIONAL FACILITIES WORK		47	08-Mar-26 08:00	06-May-26 10:00	08-Mar-26 08:00 A	05-May-26 17:00 A	0.00	0.00	0.00	0%	0%	0
PG-H-PR-LL-SP-MS-10	Football Playground Materials (Flooring, goal post, nets, paints, etc)	47	08-Mar-26 08:00	06-May-26 10:00	08-Mar-26 08:00 A	05-May-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-H-PR-LL-SP-MS-20	Tartan Floor	47	08-Mar-26 08:00	06-May-26 10:00	08-Mar-26 08:00 A	05-May-26 17:00 A	0.00	0.00	0.00	100%	100%	0
CONCRETE WORK		41	07-Mar-26 08:00	28-Apr-26 10:00	07-Mar-26 08:00 A	27-Apr-26 17:00 A	0.00	0.00	0.00	0%	0%	0
PG-H-PR-LL-CO-MS-10	Autoclaved Aerated Panel	41	07-Mar-26 08:00	28-Apr-26 10:00	07-Mar-26 08:00 A	27-Apr-26 17:00 A	0.00	0.00	0.00	100%	100%	0

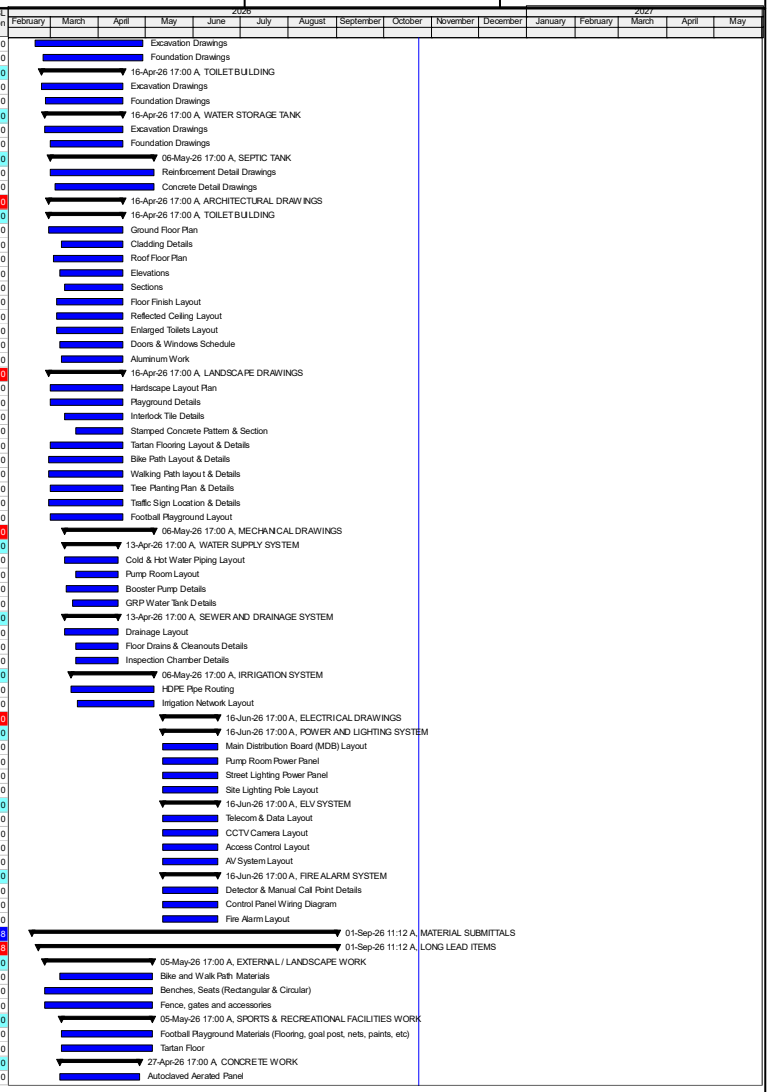


Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining W...
Milestone
summary

Baseline Schedule Rev.00

PLAYGROUNDS INITIATIVE - QASSIM, HAIL & TABUK - 25-Oct-2026

Activity ID	Activity Name	O.D	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Schedule % Complete	Performance % Complete	Variance - BL Project Duration
METAL WORK		44	11-Mar-26 08:00	06-May-26 10:00	11-Mar-26 08:00 A	05-May-26 17:00 A	0.00	0.00	0.00	0%	0%	0
PG-H-PR-LL-MT-MS-10	Metal Doors	44	11-Mar-26 08:00	06-May-26 10:00	11-Mar-26 08:00 A	05-May-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-H-PR-LL-MT-MS-20	Curtain Wall	44	11-Mar-26 08:00	06-May-26 10:00	11-Mar-26 08:00 A	05-May-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PLUMBING WORK		44	11-Mar-26 08:00	06-May-26 10:00	11-Mar-26 08:00 A	05-May-26 17:00 A	0.00	0.00	0.00	0%	0%	0
PG-H-PR-LL-PB-MS-10	Booster Pump	44	11-Mar-26 08:00	06-May-26 10:00	11-Mar-26 08:00 A	05-May-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-H-PR-LL-PB-MS-20	GRP Sectional Panel Water Tanks (4x3x3m)	40	16-Mar-26 08:00	06-May-26 10:00	16-Mar-26 08:00 A	05-May-26 17:00 A	0.00	0.00	0.00	100%	100%	0
IRRIGATION WORK		60	21-Feb-26 08:00	07-May-26 10:00	21-Feb-26 08:00 A	06-May-26 17:00 A	0.00	0.00	0.00	0%	0%	0
PG-H-PR-LL-IR-MS-10	HDPE Pipes	60	21-Feb-26 08:00	07-May-26 10:00	21-Feb-26 08:00 A	06-May-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-H-PR-LL-IR-MS-20	Irrigation Control System	60	21-Feb-26 08:00	07-May-26 10:00	21-Feb-26 08:00 A	06-May-26 17:00 A	0.00	0.00	0.00	100%	100%	0
ELECTRICAL WORK		99	12-May-26 08:00	06-Jul-26 17:00	12-May-26 08:00 A	01-Sep-26 11:12 A	0.00	0.00	0.00	0%	0%	-48
PG-H-PR-LL-EL-MS-10	Main Distribution Board(Completed)	34	12-May-26 08:00	25-Jun-26 10:00	12-May-26 08:00 A	24-Jun-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-H-PR-LL-EL-MS-10_R	Main Distribution Board(Remaining)	8	25-Jun-26 08:00	04-Jul-26 17:00	11-Jul-26 08:00 A	03-Aug-26 17:00 A	0.00	0.00	0.00	100%	100%	-13
PG-H-PR-LL-EL-MS-20	Power Panels (Pump, Street Light)(Completed)	34	12-May-26 08:00	25-Jun-26 10:00	12-May-26 08:00 A	24-Jun-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-H-PR-LL-EL-MS-20_R	Power Panels (Pump, Street Light)(Remaining)	8	25-Jun-26 08:00	04-Jul-26 17:00	11-Jul-26 08:00 A	03-Aug-26 17:00 A	0.00	0.00	0.00	100%	100%	-13
PG-H-PR-LL-EL-MS-30	Site Lighting Poles(Completed)	34	12-May-26 08:00	25-Jun-26 10:00	12-May-26 08:00 A	24-Jun-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-H-PR-LL-EL-MS-30_R	Site Lighting Poles(Remaining)	10	25-Jun-26 08:00	06-Jul-26 17:00	11-Jul-26 08:00 A	03-Aug-26 17:00 A	0.00	0.00	0.00	100%	100%	-11
PG-H-PR-LL-EL-MS-40	Lighting Fixtures(Completed)	34	12-May-26 08:00	25-Jun-26 10:00	12-May-26 08:00 A	24-Jun-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-H-PR-LL-EL-MS-40_R	Lighting Fixtures(Remaining)	10	25-Jun-26 08:00	06-Jul-26 17:00	11-Jul-26 08:00 A	23-Jul-26 17:00 A	0.00	0.00	0.00	100%	100%	-2
PG-H-PR-LL-EL-MS-50	Grounding System Materials (Earth pit rod, LPS, etc)(Completed)	34	12-May-26 08:00	25-Jun-26 10:00	12-May-26 08:00 A	24-Jun-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-H-PR-LL-EL-MS-50_R	Grounding System Materials (Earth pit rod, LPS, etc)(Remaining)	7	25-Jun-26 08:00	02-Jul-26 17:00	11-Jul-26 08:00 A	01-Sep-26 11:12 A	0.00	0.00	0.00	100%	100%	-38
PG-H-PR-LL-EL-MS-60	Telecommunications & Data System Materials (Telephone outlet, CCTV,	34	12-May-26 08:00	25-Jun-26 10:00	12-May-26 08:00 A	24-Jun-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-H-PR-LL-EL-MS-60_R	Telecommunications & Data System Materials (Telephone outlet, CCTV,	10	25-Jun-26 08:00	06-Jul-26 17:00	11-Jul-26 08:00 A	01-Sep-26 11:12 A	0.00	0.00	0.00	100%	100%	-35
PG-H-PR-LL-EL-MS-70	Security and Access Control System Materials(Completed)	34	12-May-26 08:00	25-Jun-26 10:00	12-May-26 08:00 A	24-Jun-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-H-PR-LL-EL-MS-70_R	Security and Access Control System Materials(Remaining)	10	25-Jun-26 08:00	06-Jul-26 17:00	11-Jul-26 08:00 A	01-Sep-26 11:12 A	0.00	0.00	0.00	100%	100%	-35
PG-H-PR-LL-EL-MS-80	Fire Alarm System Materials(Completed)	34	12-May-26 08:00	25-Jun-26 10:00	12-May-26 08:00 A	24-Jun-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-H-PR-LL-EL-MS-80_R	Fire Alarm System Materials(Remaining)	10	25-Jun-26 08:00	06-Jul-26 17:00	27-Aug-26 08:00 A	01-Sep-26 11:12 A	0.00	0.00	0.00	100%	100%	6
SHORT LEAD ITEMS		28	17-Feb-26 08:00	28-Mar-26 10:00	17-Feb-26 08:00 A	26-Mar-26 17:00 A	0.00	0.00	0.00	0%	0%	0
EXTERNAL / LANDSCAPE WORK		23	17-Feb-26 08:00	17-Mar-26 10:00	17-Feb-26 08:00 A	16-Mar-26 17:00 A	0.00	0.00	0.00	0%	0%	0
PG-H-PR-SL-LS-MS-10	Backfilling Materials	23	17-Feb-26 08:00	17-Mar-26 10:00	17-Feb-26 08:00 A	16-Mar-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-H-PR-SL-LS-MS-20	Interlock tiles	4	12-Mar-26 08:00	17-Mar-26 10:00	12-Mar-26 08:00 A	16-Mar-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-H-PR-SL-LS-MS-30	Compacted Natural Ground Soil	20	21-Feb-26 08:00	17-Mar-26 10:00	21-Feb-26 08:00 A	16-Mar-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-H-PR-SL-LS-MS-40	Curb Stone	4	12-Mar-26 08:00	17-Mar-26 10:00	12-Mar-26 08:00 A	16-Mar-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-H-PR-SL-LS-MS-50	Thermoplastic pavement road marking	4	12-Mar-26 08:00	17-Mar-26 10:00	12-Mar-26 08:00 A	16-Mar-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-H-PR-SL-LS-MS-60	Traffic Signages	8	08-Mar-26 08:00	17-Mar-26 10:00	08-Mar-26 08:00 A	16-Mar-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-H-PR-SL-LS-MS-70	Trees	4	12-Mar-26 08:00	17-Mar-26 10:00	12-Mar-26 08:00 A	16-Mar-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-H-PR-SL-LS-MS-80	Lawn	4	12-Mar-26 08:00	17-Mar-26 10:00	12-Mar-26 08:00 A	16-Mar-26 17:00 A	0.00	0.00	0.00	100%	100%	0
CONCRETE WORK		28	17-Feb-26 08:00	28-Mar-26 10:00	17-Feb-26 08:00 A	26-Mar-26 17:00 A	0.00	0.00	0.00	0%	0%	0
PG-H-PR-SL-CO-MS-10	Steel Rebar	17	17-Feb-26 08:00	10-Mar-26 10:00	17-Feb-26 08:00 A	09-Mar-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-H-PR-SL-CO-MS-20	Concrete	13	23-Feb-26 08:00	10-Mar-26 10:00	23-Feb-26 08:00 A	09-Mar-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-H-PR-SL-CO-MS-30	Screed	10	11-Mar-26 08:00	28-Mar-26 10:00	11-Mar-26 08:00 A	26-Mar-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-H-PR-SL-CO-MS-40	CMU Block	19	01-Mar-26 08:00	28-Mar-26 10:00	01-Mar-26 08:00 A	26-Mar-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-H-PR-SL-CO-MS-50	Concrete Repair & Protection Materials	19	01-Mar-26 08:00	28-Mar-26 10:00	01-Mar-26 08:00 A	26-Mar-26 17:00 A	0.00	0.00	0.00	100%	100%	0
ARCHITECTURAL & FINISHES WORK		4	10-Mar-26 08:00	15-Mar-26 10:00	10-Mar-26 08:00 A	14-Mar-26 17:00 A	0.00	0.00	0.00	0%	0%	0
PG-H-PR-SL-AR-MS-10	Ceramic tiles	4	10-Mar-26 08:00	15-Mar-26 10:00	10-Mar-26 08:00 A	14-Mar-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-H-PR-SL-AR-MS-100	Gypsum Boards	4	10-Mar-26 08:00	15-Mar-26 10:00	10-Mar-26 08:00 A	14-Mar-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-H-PR-SL-AR-MS-110	Specialities Materials (Toilet accessories, lockers, logo, etc)	4	10-Mar-26 08:00	15-Mar-26 10:00	10-Mar-26 08:00 A	14-Mar-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-H-PR-SL-AR-MS-120	Waterproofing System Materials	4	10-Mar-26 08:00	15-Mar-26 10:00	10-Mar-26 08:00 A	14-Mar-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-H-PR-SL-AR-MS-20	Anti-slip Granite tiles	4	10-Mar-26 08:00	15-Mar-26 10:00	10-Mar-26 08:00 A	14-Mar-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-H-PR-SL-AR-MS-30	Epoxy Paint	4	10-Mar-26 08:00	15-Mar-26 10:00	10-Mar-26 08:00 A	14-Mar-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-H-PR-SL-AR-MS-40	Cement Plaster	4	10-Mar-26 08:00	15-Mar-26 10:00	10-Mar-26 08:00 A	14-Mar-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-H-PR-SL-AR-MS-50	Acrylic Paint	4	10-Mar-26 08:00	15-Mar-26 10:00	10-Mar-26 08:00 A	14-Mar-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-H-PR-SL-AR-MS-60	Stone Cladding	4	10-Mar-26 08:00	15-Mar-26 10:00	10-Mar-26 08:00 A	14-Mar-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-H-PR-SL-AR-MS-70	Aluminum Plates	4	10-Mar-26 08:00	15-Mar-26 10:00	10-Mar-26 08:00 A	14-Mar-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-H-PR-SL-AR-MS-80	Phenolic Partition	4	10-Mar-26 08:00	15-Mar-26 10:00	10-Mar-26 08:00 A	14-Mar-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-H-PR-SL-AR-MS-90	Glass Partition	4	10-Mar-26 08:00	15-Mar-26 10:00	10-Mar-26 08:00 A	14-Mar-26 17:00 A	0.00	0.00	0.00	100%	100%	0
METAL WORK		9	07-Mar-26 08:00	17-Mar-26 10:00	07-Mar-26 08:00 A	16-Mar-26 17:00 A	0.00	0.00	0.00	0%	0%	0
PG-H-PR-SL-MT-MS-10	Galvanized Steel Ladder	4	12-Mar-26 08:00	17-Mar-26 10:00	12-Mar-26 08:00 A	16-Mar-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-H-PR-SL-MT-MS-20	Galvanized Steel Roof Scupper	9	07-Mar-26 08:00	17-Mar-26 10:00	07-Mar-26 08:00 A	16-Mar-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-H-PR-SL-MT-MS-30	Galvanized Steel Cover with frame	9	07-Mar-26 08:00	17-Mar-26 10:00	07-Mar-26 08:00 A	16-Mar-26 17:00 A	0.00	0.00	0.00	100%	100%	0
HVAC WORK		19	23-Feb-26 08:00	17-Mar-26 10:00	23-Feb-26 08:00 A	16-Mar-26 17:00 A	0.00	0.00	0.00	0%	0%	0
PG-H-PR-SL-AC-MS-10	Split Air Conditioning Unit	19	23-Feb-26 08:00	17-Mar-26 10:00	23-Feb-26 08:00 A	16-Mar-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-H-PR-SL-AC-MS-20	Air Duct	15	28-Feb-26 08:00	17-Mar-26 10:00	28-Feb-26 08:00 A	16-Mar-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-H-PR-SL-AC-MS-30	Diffusers and Grills	11	04-Mar-26 08:00	17-Mar-26 10:00	04-Mar-26 08:00 A	16-Mar-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-H-PR-SL-AC-MS-40	Exhaust fans	11	04-Mar-26 08:00	17-Mar-26 10:00	04-Mar-26 08:00 A	16-Mar-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PLUMBING WORK		4	12-Mar-26 08:00	17-Mar-26 10:00	12-Mar-26 08:00 A	16-Mar-26 17:00 A	0.00	0.00	0.00	0%	0%	0
PG-H-PR-SL-PB-MS-10	PPR Pipes & Valves	4	12-Mar-26 08:00	17-Mar-26 10:00	12-Mar-26 08:00 A	16-Mar-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-H-PR-SL-PB-MS-20	UPCV Pipes	4	12-Mar-26 08:00	17-Mar-26 10:00	12-Mar-26 08:00 A	16-Mar-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-H-PR-SL-PB-MS-30	Sanitary Drainage Fixtures	4	12-Mar-26 08:00	17-Mar-26 10:00	12-Mar-26 08:00 A	16-Mar-26 17:00 A	0.00	0.00	0.00	100%	100%	0
IRRIGATION WORK		4	12-Mar-26 08:00	17-Mar-26 10:00	12-Mar-26 08:00 A	16-Mar-26 17:00 A	0.00	0.00	0.00	0%	0%	0
PG-H-PR-SL-IR-MS-10	Gate Valve including valve box	4	12-Mar-26 08:00	17-Mar-26 10:00	12-Mar-26 08:00 A	16-Mar-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-H-PR-SL-IR-MS-20	Bubblers and Sprayers	4	12-Mar-26 08:00	17-Mar-26 10:00	12-Mar-26 08:00 A	16-Mar-26 17:00 A	0.00	0.00	0.00	100%	100%	0
ELECTRICAL WORK		4	12-Mar-26 08:00	17-Mar-26 10:00	12-Mar-26 08:00 A	16-Mar-26 17:00 A	0.00	0.00	0.00	0%	0%	0
PG-H-PR-SL-EL-MS-10	Wiring Devices Materials	4	12-Mar-26 08:00	17-Mar-26 10:00	12-Mar-26 08:00 A	16-Mar-26 17:00 A	0.00	0.00	0.00	100%	100%	0

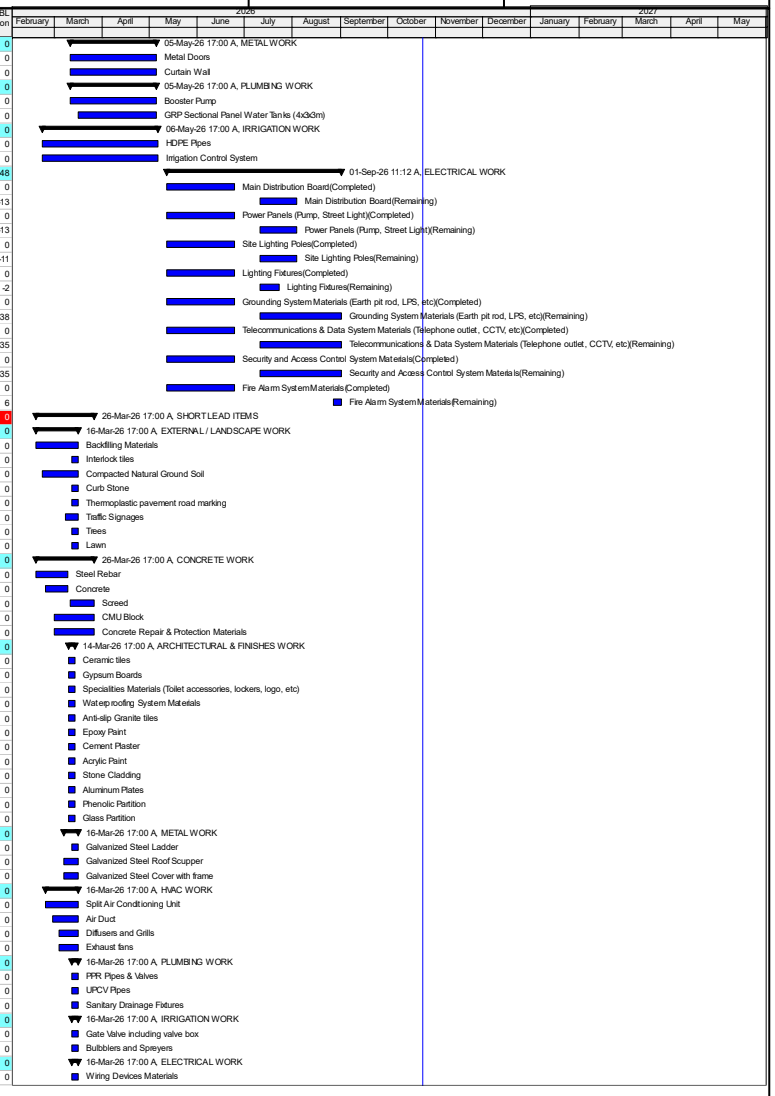


Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining W...
Milestone
summary

Baseline Schedule Rev.00

PLAYGROUNDS INITIATIVE - QASSIM, HAIL & TABUK - 25-Oct-2026

Activity ID	Activity Name	O.D	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Schedule % Complete	Performance % Complete	Variance - BL Project Duration
FIRE FIGHTING WORK		4	12-Mar-26 08:00	17-Mar-26 10:00	12-Mar-26 08:00 A	16-Mar-26 17:00 A	0.00	0.00	0.00	0%	0%	0
PG-H-PR-SL-FF-MS-10	Fire Extinguishers	4	12-Mar-26 08:00	17-Mar-26 10:00	12-Mar-26 08:00 A	16-Mar-26 17:00 A	0.00	0.00	0.00	100%	100%	0
MATERIAL APPROVALS		165	21-Feb-26 08:00	14-Jul-26 17:00	21-Feb-26 08:00 A	17-Sep-26 17:00 A	204,439.56	204,439.56	204,439.56	100%	100%	-56
LONG LEAD ITEMS		162	25-Feb-26 08:00	14-Jul-26 17:00	25-Feb-26 08:00 A	17-Sep-26 17:00 A	111,065.49	111,065.49	111,065.49	100%	100%	-56
EXTERNAL / LANDSCAPE WORK		57	25-Feb-26 08:00	06-May-26 17:00	25-Feb-26 08:00 A	06-May-26 17:00 A	26,079.63	26,079.63	26,079.63	100%	100%	0
PG-H-PR-LL-LS-MA-10	Bike and Walk Path Materials	41	16-Mar-26 08:00	06-May-26 17:00	16-Mar-26 08:00 A	06-May-26 17:00 A	16,461.00	16,461.00	16,461.00	100%	100%	0
PG-H-PR-LL-LS-MA-20	Benches, Seats (Rectangular & Circular)	57	25-Feb-26 08:00	06-May-26 17:00	25-Feb-26 08:00 A	06-May-26 17:00 A	6,327.69	6,327.69	6,327.69	100%	100%	0
PG-H-PR-LL-LS-MA-30	Fence, gates and accessories	51	04-Mar-26 08:00	06-May-26 17:00	04-Mar-26 08:00 A	06-May-26 17:00 A	3,290.94	3,290.94	3,290.94	100%	100%	0
SPORTS & RECREATIONAL FACILITIES WORK		43	14-Mar-26 08:00	06-May-26 17:00	14-Mar-26 08:00 A	06-May-26 17:00 A	38,839.50	38,839.50	38,839.50	100%	100%	0
PG-H-PR-LL-SP-MA-10	Football Playground Materials (Flooring, goal post, nets, paints, etc)	42	15-Mar-26 08:00	06-May-26 17:00	15-Mar-26 08:00 A	06-May-26 17:00 A	14,269.50	14,269.50	14,269.50	100%	100%	0
PG-H-PR-LL-SP-MA-20	Tartan Floor	43	14-Mar-26 08:00	06-May-26 17:00	14-Mar-26 08:00 A	06-May-26 17:00 A	24,570.00	24,570.00	24,570.00	100%	100%	0
CONCRETE WORK		45	11-Mar-26 08:00	06-May-26 17:00	11-Mar-26 08:00 A	06-May-26 17:00 A	1,417.50	1,417.50	1,417.50	100%	100%	0
PG-H-PR-LL-CO-MA-10	Autoclaved Aerated Panel	45	11-Mar-26 08:00	06-May-26 17:00	11-Mar-26 08:00 A	06-May-26 17:00 A	1,417.50	1,417.50	1,417.50	100%	100%	0
METAL WORK		42	15-Mar-26 08:00	06-May-26 17:00	15-Mar-26 08:00 A	06-May-26 17:00 A	889.23	889.23	889.23	100%	100%	0
PG-H-PR-LL-MT-MA-10	Metal Doors	42	15-Mar-26 08:00	06-May-26 17:00	15-Mar-26 08:00 A	06-May-26 17:00 A	127.53	127.53	127.53	100%	100%	0
PG-H-PR-LL-MT-MA-20	Curtain Wall	42	15-Mar-26 08:00	06-May-26 17:00	15-Mar-26 08:00 A	06-May-26 17:00 A	761.70	761.70	761.70	100%	100%	0
PLUMBING WORK		41	16-Mar-26 08:00	06-May-26 17:00	16-Mar-26 08:00 A	06-May-26 17:00 A	3,553.95	3,553.95	3,553.95	100%	100%	0
PG-H-PR-LL-PB-MA-10	Booster Pump	41	16-Mar-26 08:00	06-May-26 17:00	16-Mar-26 08:00 A	06-May-26 17:00 A	1,818.30	1,818.30	1,818.30	100%	100%	0
PG-H-PR-LL-PB-MA-20	GRP Sectional Panel Water Tanks (4x3x3m)	38	24-Mar-26 08:00	06-May-26 17:00	24-Mar-26 08:00 A	06-May-26 17:00 A	1,735.65	1,735.65	1,735.65	100%	100%	0
IRRIGATION WORK		55	28-Feb-26 08:00	06-May-26 17:00	28-Feb-26 08:00 A	06-May-26 17:00 A	12,818.25	12,818.25	12,818.25	100%	100%	0
PG-H-PR-LL-IR-MA-10	HDPE Pipes	55	28-Feb-26 08:00	06-May-26 17:00	28-Feb-26 08:00 A	06-May-26 17:00 A	8,272.50	8,272.50	8,272.50	100%	100%	0
PG-H-PR-LL-IR-MA-20	Irrigation Control System	55	28-Feb-26 08:00	06-May-26 17:00	28-Feb-26 08:00 A	06-May-26 17:00 A	4,545.75	4,545.75	4,545.75	100%	100%	0
ELECTRICAL WORK		101	12-May-26 08:00	14-Jul-26 17:00	12-May-26 08:00 A	17-Sep-26 17:00 A	27,467.43	27,467.43	27,467.43	100%	100%	-56
PG-H-PR-LL-EL-MA-10	Main Distribution Board(Completed)	34	12-May-26 08:00	24-Jun-26 17:00	12-May-26 08:00 A	24-Jun-26 17:00 A	347.13	347.13	347.13	100%	100%	0
PG-H-PR-LL-EL-MA-10_R	Main Distribution Board(Remaining)	10	25-Jun-26 08:00	06-Jul-26 17:00	30-Jul-26 08:00 A	17-Sep-26 17:00 A	148.77	148.77	148.77	100%	100%	-33
PG-H-PR-LL-EL-MA-20	Power Panels (Pump, Street Light)(Completed)	34	12-May-26 08:00	24-Jun-26 17:00	12-May-26 08:00 A	24-Jun-26 17:00 A	277.70	277.70	277.70	100%	100%	0
PG-H-PR-LL-EL-MA-20_R	Power Panels (Pump, Street Light)(Remaining)	10	25-Jun-26 08:00	06-Jul-26 17:00	30-Jul-26 08:00 A	17-Sep-26 17:00 A	119.02	119.02	119.02	100%	100%	-33
PG-H-PR-LL-EL-MA-30	Site Lighting Poles(Completed)	34	12-May-26 08:00	24-Jun-26 17:00	12-May-26 08:00 A	24-Jun-26 17:00 A	14,891.18	14,891.18	14,891.18	100%	100%	0
PG-H-PR-LL-EL-MA-30_R	Site Lighting Poles(Remaining)	10	25-Jun-26 08:00	06-Jul-26 17:00	30-Jul-26 08:00 A	17-Sep-26 17:00 A	6,381.94	6,381.94	6,381.94	100%	100%	-33
PG-H-PR-LL-EL-MA-40	Lighting Fixtures(Completed)	34	12-May-26 08:00	24-Jun-26 17:00	12-May-26 08:00 A	24-Jun-26 17:00 A	897.98	897.98	897.98	100%	100%	0
PG-H-PR-LL-EL-MA-40_R	Lighting Fixtures(Remaining)	10	25-Jun-26 08:00	06-Jul-26 17:00	23-Jul-26 08:00 A	23-Jul-26 17:00 A	384.85	384.85	384.85	100%	100%	9
PG-H-PR-LL-EL-MA-50	Grounding System Materials (Earth pit rod, LPS, etc)(Completed)	34	12-May-26 08:00	24-Jun-26 17:00	12-May-26 08:00 A	24-Jun-26 17:00 A	702.93	702.93	702.93	100%	100%	0
PG-H-PR-LL-EL-MA-50_R	Grounding System Materials (Earth pit rod, LPS, etc)(Remaining)	10	04-Jul-26 08:00	14-Jul-26 17:00	27-Aug-26 08:00 A	17-Sep-26 17:00 A	301.26	301.26	301.26	100%	100%	-9
PG-H-PR-LL-EL-MA-60	Telecommunications & Data System Materials (Telephone outlet, CCTV,	34	12-May-26 08:00	24-Jun-26 17:00	12-May-26 08:00 A	24-Jun-26 17:00 A	685.57	685.57	685.57	100%	100%	0
PG-H-PR-LL-EL-MA-60_R	Telecommunications & Data System Materials (Telephone outlet, CCTV,	10	25-Jun-26 08:00	06-Jul-26 17:00	27-Aug-26 08:00 A	17-Sep-26 17:00 A	293.81	293.81	293.81	100%	100%	-9
PG-H-PR-LL-EL-MA-70	Security and Access Control System Materials(Completed)	34	12-May-26 08:00	24-Jun-26 17:00	12-May-26 08:00 A	24-Jun-26 17:00 A	867.93	867.93	867.93	100%	100%	0
PG-H-PR-LL-EL-MA-70_R	Security and Access Control System Materials(Remaining)	10	25-Jun-26 08:00	06-Jul-26 17:00	27-Aug-26 08:00 A	17-Sep-26 17:00 A	371.97	371.97	371.97	100%	100%	-9
PG-H-PR-LL-EL-MA-80	Fire Alarm System Materials(Completed)	34	12-May-26 08:00	24-Jun-26 17:00	12-May-26 08:00 A	24-Jun-26 17:00 A	556.77	556.77	556.77	100%	100%	0
PG-H-PR-LL-EL-MA-80_R	Fire Alarm System Materials(Remaining)	10	25-Jun-26 08:00	06-Jul-26 17:00	27-Aug-26 08:00 A	17-Sep-26 17:00 A	238.62	238.62	238.62	100%	100%	-9
SHORT LEAD ITEMS		25	21-Feb-26 08:00	26-Mar-26 17:00	21-Feb-26 08:00 A	26-Mar-26 17:00 A	93,374.07	93,374.07	93,374.07	100%	100%	0
EXTERNAL / LANDSCAPE WORK		25	21-Feb-26 08:00	26-Mar-26 17:00	21-Feb-26 08:00 A	26-Mar-26 17:00 A	72,133.44	72,133.44	72,133.44	100%	100%	0
PG-H-PR-SL-LS-MA-10	Backfilling Materials	25	21-Feb-26 08:00	26-Mar-26 17:00	21-Feb-26 08:00 A	26-Mar-26 17:00 A	19,575.00	19,575.00	19,575.00	100%	100%	0
PG-H-PR-SL-LS-MA-20	Interlock tiles	2	25-Mar-26 08:00	26-Mar-26 17:00	25-Mar-26 08:00 A	26-Mar-26 17:00 A	17,494.50	17,494.50	17,494.50	100%	100%	0
PG-H-PR-SL-LS-MA-30	Compacted Natural Ground Soil	22	25-Feb-26 08:00	26-Mar-26 17:00	25-Feb-26 08:00 A	26-Mar-26 17:00 A	3,120.00	3,120.00	3,120.00	100%	100%	0
PG-H-PR-SL-LS-MA-40	Curb Stone	2	25-Mar-26 08:00	26-Mar-26 17:00	25-Mar-26 08:00 A	26-Mar-26 17:00 A	20,928.00	20,928.00	20,928.00	100%	100%	0
PG-H-PR-SL-LS-MA-50	Thermoplastic pavement road marking	2	25-Mar-26 08:00	26-Mar-26 17:00	25-Mar-26 08:00 A	26-Mar-26 17:00 A	525.63	525.63	525.63	100%	100%	0
PG-H-PR-SL-LS-MA-60	Traffic Signages	10	11-Mar-26 08:00	26-Mar-26 17:00	11-Mar-26 08:00 A	26-Mar-26 17:00 A	198.36	198.36	198.36	100%	100%	0
PG-H-PR-SL-LS-MA-70	Trees	7	15-Mar-26 08:00	26-Mar-26 17:00	15-Mar-26 08:00 A	26-Mar-26 17:00 A	4,831.95	4,831.95	4,831.95	100%	100%	0
PG-H-PR-SL-LS-MA-80	Lawn	7	15-Mar-26 08:00	26-Mar-26 17:00	15-Mar-26 08:00 A	26-Mar-26 17:00 A	5,460.00	5,460.00	5,460.00	100%	100%	0
CONCRETE WORK		24	23-Feb-26 08:00	26-Mar-26 17:00	23-Feb-26 08:00 A	26-Mar-26 17:00 A	1,609.47	1,609.47	1,609.47	100%	100%	0
PG-H-PR-SL-CO-MA-10	Steel Rebar	14	23-Feb-26 08:00	10-Mar-26 17:00	23-Feb-26 08:00 A	10-Mar-26 17:00 A	476.82	476.82	476.82	100%	100%	0
PG-H-PR-SL-CO-MA-20	Concrete	9	01-Mar-26 08:00	10-Mar-26 17:00	01-Mar-26 08:00 A	10-Mar-26 17:00 A	518.85	518.85	518.85	100%	100%	0
PG-H-PR-SL-CO-MA-30	Screed	1	26-Mar-26 08:00	26-Mar-26 17:00	26-Mar-26 08:00 A	26-Mar-26 17:00 A	117.60	117.60	117.60	100%	100%	0
PG-H-PR-SL-CO-MA-40	CMU Block	15	05-Mar-26 08:00	26-Mar-26 17:00	05-Mar-26 08:00 A	26-Mar-26 17:00 A	124.20	124.20	124.20	100%	100%	0
PG-H-PR-SL-CO-MA-50	Concrete Repair & Protection Materials	15	05-Mar-26 08:00	26-Mar-26 17:00	05-Mar-26 08:00 A	26-Mar-26 17:00 A	372.00	372.00	372.00	100%	100%	0
ARCHITECTURAL & FINISHES WORK		2	15-Mar-26 08:00	16-Mar-26 17:00	15-Mar-26 08:00 A	16-Mar-26 17:00 A	8,114.01	8,114.01	8,114.01	100%	100%	0
PG-H-PR-SL-AR-MA-10	Ceramic tiles	2	15-Mar-26 08:00	16-Mar-26 17:00	15-Mar-26 08:00 A	16-Mar-26 17:00 A	571.95	571.95	571.95	100%	100%	0
PG-H-PR-SL-AR-MA-100	Gypsum Boards	2	15-Mar-26 08:00	16-Mar-26 17:00	15-Mar-26 08:00 A	16-Mar-26 17:00 A	188.58	188.58	188.58	100%	100%	0
PG-H-PR-SL-AR-MA-110	Specialities Materials (Toilet accessories, lockers, logo, etc)	2	15-Mar-26 08:00	16-Mar-26 17:00	15-Mar-26 08:00 A	16-Mar-26 17:00 A	2,262.87	2,262.87	2,262.87	100%	100%	0
PG-H-PR-SL-AR-MA-120	Waterproofing System Materials	2	15-Mar-26 08:00	16-Mar-26 17:00	15-Mar-26 08:00 A	16-Mar-26 17:00 A	544.20	544.20	544.20	100%	100%	0
PG-H-PR-SL-AR-MA-20	Anti-slip Granite tiles	2	15-Mar-26 08:00	16-Mar-26 17:00	15-Mar-26 08:00 A	16-Mar-26 17:00 A	535.50	535.50	535.50	100%	100%	0
PG-H-PR-SL-AR-MA-30	Epoxy Paint	2	15-Mar-26 08:00	16-Mar-26 17:00	15-Mar-26 08:00 A	16-Mar-26 17:00 A	111.18	111.18	111.18	100%	100%	0
PG-H-PR-SL-AR-MA-40	Cement Plaster	2	15-Mar-26 08:00	16-Mar-26 17:00	15-Mar-26 08:00 A	16-Mar-26 17:00 A	221.37	221.37	221.37	100%	100%	0
PG-H-PR-SL-AR-MA-50	Acrylic Paint	2	15-Mar-26 08:00	16-Mar-26 17:00	15-Mar-26 08:00 A	16-Mar-26 17:00 A	147.90	147.90	147.90	100%	100%	0
PG-H-PR-SL-AR-MA-60	Stone Cladding	2	15-Mar-26 08:00	16-Mar-26 17:00	15-Mar-26 08:00 A	16-Mar-26 17:00 A	1,852.20	1,852.20	1,852.20	100%	100%	0
PG-H-PR-SL-AR-MA-70	Aluminum Plates	2	15-Mar-26 08:00	16-Mar-26 17:00	15-Mar-26 08:00 A	16-Mar-26 17:00 A	182.46	182.46	182.46	100%	100%	0
PG-H-PR-SL-AR-MA-80	Phenolic Partition	2	15-Mar-26 08:00	16-Mar-26 17:00	15-Mar-26 08:00 A	16-Mar-26 17:00 A	1,340.40	1,340.40	1,340.40	100%	100%	0
PG-H-PR-SL-AR-MA-90	Glass Partition	2	15-Mar-26 08:00	16-Mar-26 17:00	15-Mar-26 08:00 A	16-Mar-26 17:00 A	155.40	155.40	155.40	100%	100%	0
METAL WORK		10	11-Mar-26 08:00	26-Mar-26 17:00	11-Mar-26 08:00 A	26-Mar-26 17:00 A	478.89	478.89	478.89	100%	100%	0
PG-H-PR-SL-MT-MA-10	Galvanized Steel Ladder	7	15-Mar-26 08:00	26-Mar-26 17:00	15-Mar-26 08:00 A	26-Mar-26 17:00 A	361.86	361.86	361.86	100%	100%	0
PG-H-PR-SL-MT-MA-20	Galvanized Steel Roof Scupper	10	11-Mar-26 08:00	26-Mar-26 17:00	11-Mar-26 08:00 A	26-Mar-26 17:00 A	31.32	31.32	31.32	100%	100%	0
PG-H-PR-SL-MT-MA-30	Galvanized Steel Cover with frame	10	11-Mar-26 08:00	26-Mar-26 17:00	11-Mar-26 08:00 A	26-Mar-26 17:00 A	85.71	85.71	85.71	100%	100%	0
HVAC WORK		20	28-Feb-26 08:00	26-Mar-26 17:00	28-Feb-26 08:00 A	26-Mar-26 17:00 A	606.36	606.36	606.36	100%	100%	0

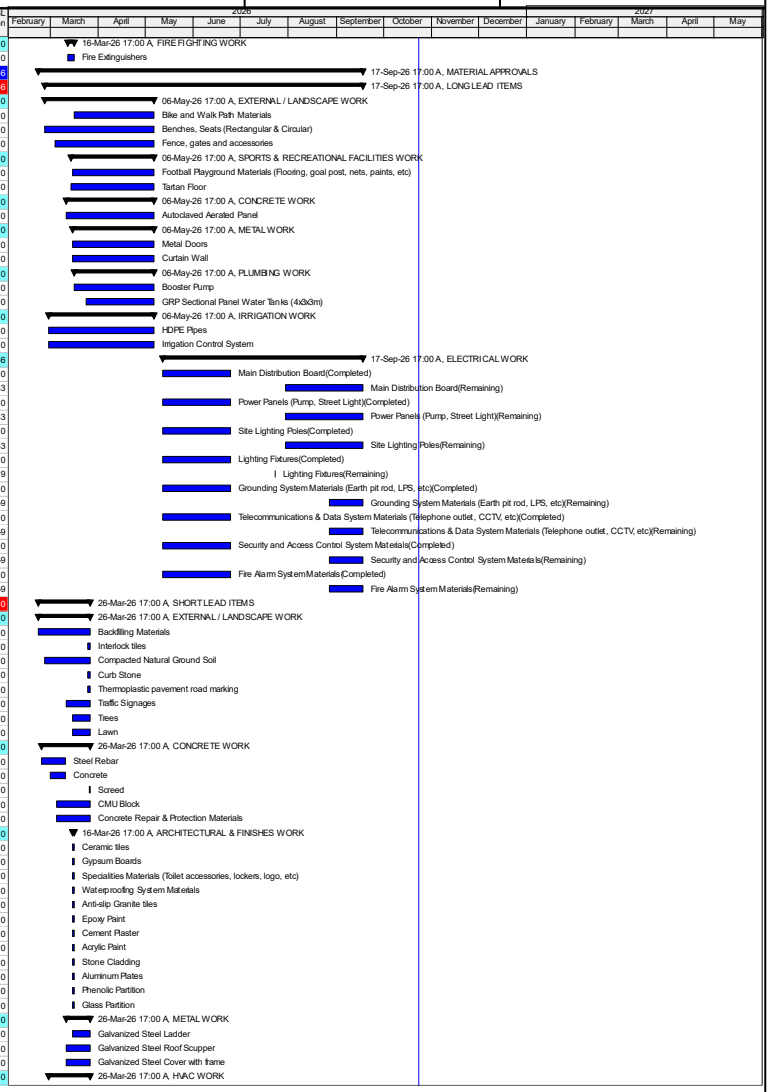


Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining W...
Milestone
summary

Baseline Schedule Rev.00

PLAYGROUNDS INITIATIVE - QASSIM, HAIL & TABUK - 25-Oct-2026

Activity ID	Activity Name	O.D	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Schedule % Complete	Performance % Complete	Variance - BL Project Duration
PG-H-PR-SL-AC-MA-10	Split Air Conditioning Unit	20	28-Feb-26 08:00	26-Mar-26 17:00	28-Feb-26 08:00 A	26-Mar-26 17:00 A	309.93	309.93	309.93	100%	100%	0
PG-H-PR-SL-AC-MA-20	Air Duct	16	04-Mar-26 08:00	26-Mar-26 17:00	04-Mar-26 08:00 A	26-Mar-26 17:00 A	156.00	156.00	156.00	100%	100%	0
PG-H-PR-SL-AC-MA-30	Diffusers and Grills	2	25-Mar-26 08:00	26-Mar-26 17:00	25-Mar-26 08:00 A	26-Mar-26 17:00 A	74.31	74.31	74.31	100%	100%	0
PG-H-PR-SL-AC-MA-40	Exhaust fans	2	25-Mar-26 08:00	26-Mar-26 17:00	25-Mar-26 08:00 A	26-Mar-26 17:00 A	66.12	66.12	66.12	100%	100%	0
PLUMBING WORK		2	25-Mar-26 08:00	26-Mar-26 17:00	25-Mar-26 08:00 A	26-Mar-26 17:00 A	3,147.03	3,147.03	3,147.03	100%	100%	0
PG-H-PR-SL-PB-MA-10	PPR Pipes & Valves	2	25-Mar-26 08:00	26-Mar-26 17:00	25-Mar-26 08:00 A	26-Mar-26 17:00 A	265.20	265.20	265.20	100%	100%	0
PG-H-PR-SL-PB-MA-20	UPCV Pipes	2	25-Mar-26 08:00	26-Mar-26 17:00	25-Mar-26 08:00 A	26-Mar-26 17:00 A	335.19	335.19	335.19	100%	100%	0
PG-H-PR-SL-PB-MA-30	Sanitary Drainage Fixtures	2	25-Mar-26 08:00	26-Mar-26 17:00	25-Mar-26 08:00 A	26-Mar-26 17:00 A	2,546.64	2,546.64	2,546.64	100%	100%	0
IRRIGATION WORK		2	25-Mar-26 08:00	26-Mar-26 17:00	25-Mar-26 08:00 A	26-Mar-26 17:00 A	6,854.64	6,854.64	6,854.64	100%	100%	0
PG-H-PR-SL-IR-MA-10	Gate Valve including valve box	2	25-Mar-26 08:00	26-Mar-26 17:00	25-Mar-26 08:00 A	26-Mar-26 17:00 A	756.30	756.30	756.30	100%	100%	0
PG-H-PR-SL-IR-MA-20	Bubblers and Spreyers	2	25-Mar-26 08:00	26-Mar-26 17:00	25-Mar-26 08:00 A	26-Mar-26 17:00 A	6,098.34	6,098.34	6,098.34	100%	100%	0
ELECTRICAL WORK		2	25-Mar-26 08:00	26-Mar-26 17:00	25-Mar-26 08:00 A	26-Mar-26 17:00 A	407.52	407.52	407.52	100%	100%	0
PG-H-PR-SL-EL-MA-10	Wiring Devices Materials	2	25-Mar-26 08:00	26-Mar-26 17:00	25-Mar-26 08:00 A	26-Mar-26 17:00 A	407.52	407.52	407.52	100%	100%	0
FIRE FIGHTING WORK		2	25-Mar-26 08:00	26-Mar-26 17:00	25-Mar-26 08:00 A	26-Mar-26 17:00 A	22.71	22.71	22.71	100%	100%	0
PG-H-PR-SL-FF-MA-10	Fire Extinguishers	2	25-Mar-26 08:00	26-Mar-26 17:00	25-Mar-26 08:00 A	26-Mar-26 17:00 A	22.71	22.71	22.71	100%	100%	0
PROCUREMENT		215	26-Feb-26 08:00	26-Aug-26 17:00	26-Feb-26 08:00 A	26-Oct-26 11:12	1,839,956.04	1,816,202.83	1,839,956.04	100%	98.71%	-50
LONG LEAD ITEMS		209	05-Mar-26 08:00	26-Aug-26 17:00	05-Mar-26 08:00 A	26-Oct-26 11:12	999,589.41	981,462.29	999,589.41	100%	98.19%	-50
PURCHASE ORDER		162	05-Mar-26 08:00	22-Jul-26 17:00	05-Mar-26 08:00 A	08-Sep-26 11:36 A	0.00	0.00	0.00	0%	0%	-40
EXTERNAL / LANDSCAPE WORK		49	07-Mar-26 08:00	07-May-26 10:00	07-Mar-26 08:00 A	06-May-26 17:00 A	0.00	0.00	0.00	0%	0%	0
PG-H-PR-LL-LS-PO-10	Bike and Walk Path Materials	33	30-Mar-26 08:00	07-May-26 10:00	30-Mar-26 08:00 A	06-May-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-H-PR-LL-LS-PO-20	Benches, Seats (Rectangular & Circular)	49	07-Mar-26 08:00	07-May-26 10:00	07-Mar-26 08:00 A	06-May-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-H-PR-LL-LS-PO-30	Fence, gates and accessories	43	14-Mar-26 08:00	07-May-26 10:00	14-Mar-26 08:00 A	06-May-26 17:00 A	0.00	0.00	0.00	100%	100%	0
SPORTS & RECREATIONAL FACILITIES WORK		35	28-Mar-26 08:00	07-May-26 10:00	28-Mar-26 08:00 A	06-May-26 17:00 A	0.00	0.00	0.00	0%	0%	0
PG-H-PR-LL-SP-PO-10	Football Playground Materials (Flooring, goal post, nets, paints, etc)	34	29-Mar-26 08:00	07-May-26 10:00	29-Mar-26 08:00 A	06-May-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-H-PR-LL-SP-PO-20	Tartan Floor	35	28-Mar-26 08:00	07-May-26 10:00	28-Mar-26 08:00 A	06-May-26 17:00 A	0.00	0.00	0.00	100%	100%	0
CONCRETE WORK		39	18-Mar-26 08:00	07-May-26 10:00	18-Mar-26 08:00 A	06-May-26 17:00 A	0.00	0.00	0.00	0%	0%	0
PG-H-PR-LL-CO-PO-10	Autoclaved Aerated Panel	39	18-Mar-26 08:00	07-May-26 10:00	18-Mar-26 08:00 A	06-May-26 17:00 A	0.00	0.00	0.00	100%	100%	0
METAL WORK		38	24-Mar-26 08:00	07-May-26 10:00	24-Mar-26 08:00 A	06-May-26 17:00 A	0.00	0.00	0.00	0%	0%	0
PG-H-PR-LL-MT-PO-10	Metal Doors	38	24-Mar-26 08:00	07-May-26 10:00	24-Mar-26 08:00 A	06-May-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-H-PR-LL-MT-PO-20	Curtain Wall	38	24-Mar-26 08:00	07-May-26 10:00	24-Mar-26 08:00 A	06-May-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PLUMBING WORK		34	29-Mar-26 08:00	07-May-26 10:00	29-Mar-26 08:00 A	06-May-26 17:00 A	0.00	0.00	0.00	0%	0%	0
PG-H-PR-LL-PB-PO-10	Booster Pump	34	29-Mar-26 08:00	07-May-26 10:00	29-Mar-26 08:00 A	06-May-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-H-PR-LL-PB-PO-20	GRP Sectional Panel Water Tanks (4x3x3m)	33	30-Mar-26 08:00	07-May-26 10:00	30-Mar-26 08:00 A	06-May-26 17:00 A	0.00	0.00	0.00	100%	100%	0
IRRIGATION WORK		50	05-Mar-26 08:00	07-May-26 10:00	05-Mar-26 08:00 A	06-May-26 17:00 A	0.00	0.00	0.00	0%	0%	0
PG-H-PR-LL-IR-PO-10	HDPE Pipes	49	07-Mar-26 08:00	07-May-26 10:00	07-Mar-26 08:00 A	06-May-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-H-PR-LL-IR-PO-20	Irrigation Control System	50	05-Mar-26 08:00	07-May-26 10:00	05-Mar-26 08:00 A	06-May-26 17:00 A	0.00	0.00	0.00	100%	100%	0
ELECTRICAL WORK		109	11-May-26 08:00	22-Jul-26 17:00	11-May-26 08:00 A	08-Sep-26 11:36 A	0.00	0.00	0.00	0%	0%	-40
PG-H-PR-LL-EL-PO-10	Main Distribution Board(Completed)	35	11-May-26 08:00	25-Jun-26 10:00	11-May-26 08:00 A	24-Jun-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-H-PR-LL-EL-PO-10_R	Main Distribution Board(Remaining)	7	07-Jul-26 08:00	14-Jul-26 17:00	05-Aug-26 08:00 A	08-Sep-26 11:36 A	0.00	0.00	0.00	100%	100%	-22
PG-H-PR-LL-EL-PO-20	Power Panels (Pump, Street Light)(Completed)	35	11-May-26 08:00	25-Jun-26 10:00	11-May-26 08:00 A	24-Jun-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-H-PR-LL-EL-PO-20_R	Power Panels (Pump, Street Light)(Remaining)	7	07-Jul-26 08:00	14-Jul-26 17:00	05-Aug-26 08:00 A	08-Sep-26 11:36 A	0.00	0.00	0.00	100%	100%	-22
PG-H-PR-LL-EL-PO-30	Site Lighting Poles(Completed)	35	11-May-26 08:00	25-Jun-26 10:00	11-May-26 08:00 A	24-Jun-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-H-PR-LL-EL-PO-30_R	Site Lighting Poles(Remaining)	7	07-Jul-26 08:00	14-Jul-26 17:00	05-Aug-26 08:00 A	08-Sep-26 11:36 A	0.00	0.00	0.00	100%	100%	-22
PG-H-PR-LL-EL-PO-40	Lighting Fixtures(Completed)	35	11-May-26 08:00	25-Jun-26 10:00	11-May-26 08:00 A	24-Jun-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-H-PR-LL-EL-PO-40_R	Lighting Fixtures(Remaining)	7	07-Jul-26 08:00	14-Jul-26 17:00	23-Jul-26 08:00 A	23-Jul-26 17:00 A	0.00	0.00	0.00	100%	100%	6
PG-H-PR-LL-EL-PO-50	Grounding System Materials (Earth pit rod, LPS, etc)(Completed)	35	11-May-26 08:00	25-Jun-26 10:00	11-May-26 08:00 A	24-Jun-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-H-PR-LL-EL-PO-50_R	Grounding System Materials (Earth pit rod, LPS, etc)(Remaining)	7	15-Jul-26 08:00	22-Jul-26 17:00	27-Aug-26 08:00 A	08-Sep-26 11:36 A	0.00	0.00	0.00	100%	100%	-3
PG-H-PR-LL-EL-PO-60	Telecommunications & Data System Materials (Telephone outlet, CCTV,	35	11-May-26 08:00	25-Jun-26 10:00	11-May-26 08:00 A	24-Jun-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-H-PR-LL-EL-PO-60_R	Telecommunications & Data System Materials (Telephone outlet, CCTV,	7	07-Jul-26 08:00	14-Jul-26 17:00	27-Aug-26 08:00 A	08-Sep-26 11:36 A	0.00	0.00	0.00	100%	100%	-3
PG-H-PR-LL-EL-PO-70	Security and Access Control System Materials(Completed)	35	11-May-26 08:00	25-Jun-26 10:00	11-May-26 08:00 A	24-Jun-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-H-PR-LL-EL-PO-70_R	Security and Access Control System Materials(Remaining)	7	07-Jul-26 08:00	14-Jul-26 17:00	27-Aug-26 08:00 A	08-Sep-26 11:36 A	0.00	0.00	0.00	100%	100%	-3
PG-H-PR-LL-EL-PO-80	Fire Alarm System Materials(Completed)	35	11-May-26 08:00	25-Jun-26 10:00	11-May-26 08:00 A	24-Jun-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-H-PR-LL-EL-PO-80_R	Fire Alarm System Materials(Remaining)	7	07-Jul-26 08:00	14-Jul-26 17:00	27-Aug-26 08:00 A	08-Sep-26 11:36 A	0.00	0.00	0.00	100%	100%	-3
MANUFACTURE / FABRICATION		190	01-Apr-26 08:00	12-Aug-26 17:00	01-Apr-26 08:00 A	02-Oct-26 17:00 A	0.00	0.00	0.00	0%	0%	-42
EXTERNAL / LANDSCAPE WORK		103	05-May-26 08:00	23-Jul-26 17:00	05-May-26 08:00 A	10-Sep-26 08:00 A	0.00	0.00	0.00	0%	0%	-41
PG-H-PR-LL-LS-MF-10	Bike and Walk Path Materials(Completed)	40	05-May-26 08:00	25-Jun-26 10:00	05-May-26 08:00 A	24-Jun-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-H-PR-LL-LS-MF-10_R	Bike and Walk Path Materials(Remaining)	25	25-Jun-26 08:00	23-Jul-26 17:00	30-Jul-26 08:00 A	10-Sep-26 08:00 A	0.00	0.00	0.00	100%	100%	-11
PG-H-PR-LL-LS-MF-20	Benches, Seats (Rectangular & Circular)(Completed)	40	05-May-26 08:00	25-Jun-26 10:00	05-May-26 08:00 A	24-Jun-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-H-PR-LL-LS-MF-20_R	Benches, Seats (Rectangular & Circular)(Remaining)	25	25-Jun-26 08:00	23-Jul-26 17:00	05-Aug-26 08:00 A	10-Sep-26 08:00 A	0.00	0.00	0.00	100%	100%	-6
PG-H-PR-LL-LS-MF-30	Fence, gates and accessories(Completed)	40	05-May-26 08:00	25-Jun-26 10:00	05-May-26 08:00 A	24-Jun-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-H-PR-LL-LS-MF-30_R	Fence, gates and accessories(Remaining)	5	25-Jun-26 08:00	30-Jun-26 17:00	23-Jul-26 08:00 A	10-Sep-26 08:00 A	0.00	0.00	0.00	100%	100%	-37
SPORTS & RECREATIONAL FACILITIES WORK		97	05-May-26 08:00	23-Jul-26 17:00	05-May-26 08:00 A	10-Sep-26 08:00 A	0.00	0.00	0.00	0%	0%	-41
PG-H-PR-LL-SP-MF-10	Football Playground Materials (Flooring, goal post, nets, paints,	40	05-May-26 08:00	25-Jun-26 10:00	05-May-26 08:00 A	24-Jun-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-H-PR-LL-SP-MF-10_R	Football Playground Materials (Flooring, goal post, nets, paints,	25	25-Jun-26 08:00	23-Jul-26 17:00	30-Jul-26 08:00 A	10-Sep-26 08:00 A	0.00	0.00	0.00	100%	100%	-11
PG-H-PR-LL-SP-MF-20	Tartan Floor(Completed)	40	05-May-26 08:00	25-Jun-26 10:00	05-May-26 08:00 A	24-Jun-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-H-PR-LL-SP-MF-20_R	Tartan Floor(Remaining)	25	25-Jun-26 08:00	23-Jul-26 17:00	30-Jul-26 08:00 A	10-Sep-26 08:00 A	0.00	0.00	0.00	100%	100%	-11
CONCRETE WORK		93	01-Apr-26 08:00	06-Jul-26 17:00	01-Apr-26 08:00 A	27-Jun-26 17:00 A	0.00	0.00	0.00	0%	0%	8
PG-H-PR-LL-CO-MF-10	Autoclaved Aerated Panel(Completed)	69	01-Apr-26 08:00	25-Jun-26 10:00	01-Apr-26 08:00 A	24-Jun-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-H-PR-LL-CO-MF-10_R	Autoclaved Aerated Panel(Remaining)	10	25-Jun-26 08:00	06-Jul-26 17:00	24-Jun-26 08:00 A	27-Jun-26 17:00 A	0.00	0.00	0.00	100%	100%	7
METAL WORK		161	05-May-26 08:00	23-Jul-26 17:00	05-May-26 08:00 A	02-Oct-26 17:00 A	0.00	0.00	0.00	0%	0%	-59
PG-H-PR-LL-MT-MF-10	Metal Doors(Completed)	40	05-May-26 08:00	25-Jun-26 10:00	05-May-26 08:00 A	24-Jun-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-H-PR-LL-MT-MF-10_R	Metal Doors(Remaining)	25	25-Jun-26 08:00	23-Jul-26 17:00	26-Sep-26 08:00 A	02-Oct-26 17:00 A	0.00	0.00	0.00	100%	100%	19
PG-H-PR-LL-MT-MF-20	Curtain Wall(Completed)	40	05-May-26 08:00	25-Jun-26 10:00	05-May-26 08:00 A	24-Jun-26 17:00 A	0.00	0.00	0.00	100%	100%	0

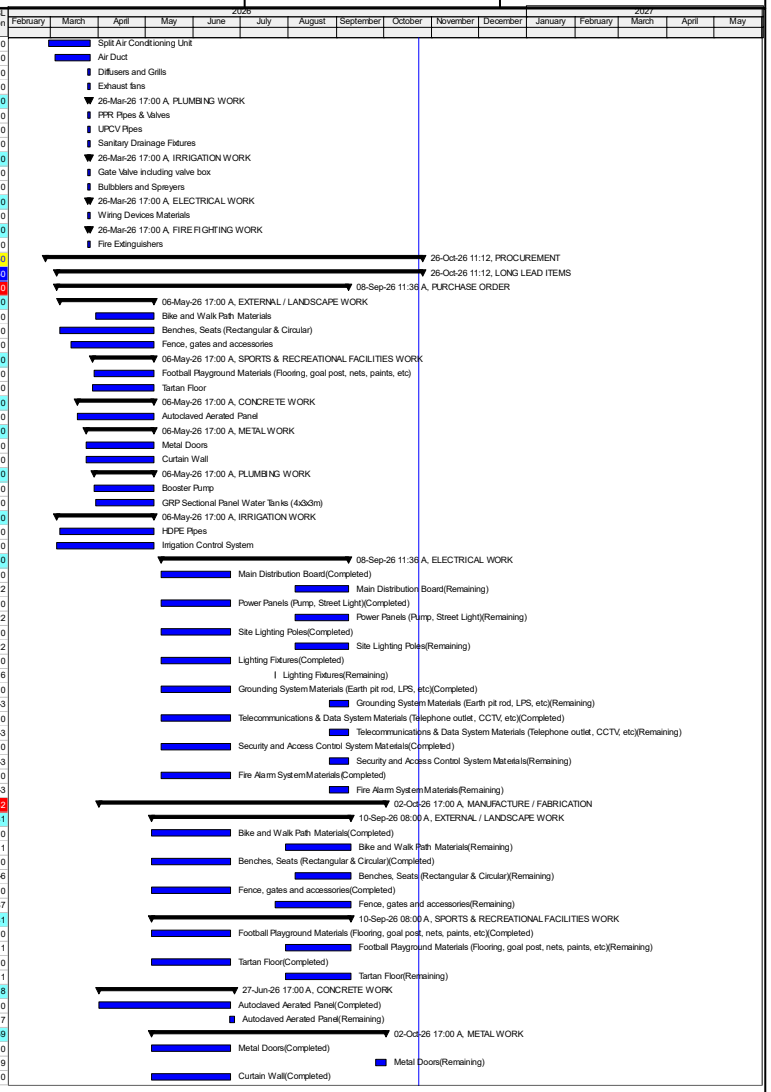


Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining W...
Milestone
summary

Baseline Schedule Rev.00

PLAYGROUNDS INITIATIVE - QASSIM, HAIL & TABUK - 25-Oct-2026

Activity ID	Activity Name	O.D	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Schedule % Complete	Performance % Complete	Variance - BL Project Duration
PG-H-PR-LL-MT-MF-20_R	Curtain Wall(Remaining)	25	25-Jun-26 08:00	23-Jul-26 17:00	17-Aug-26 08:00 A	26-Aug-26 17:00 A	0.00	0.00	0.00	100%	100%	16
PLUMBING WORK		120	05-May-26 08:00	23-Jul-26 17:00	05-May-26 08:00 A	10-Sep-26 08:00 A	0.00	0.00	0.00	0%	0%	-41
PG-H-PR-LL-PB-MF-10	Booster Pump(Completed)	40	05-May-26 08:00	25-Jun-26 10:00	05-May-26 08:00 A	24-Jun-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-H-PR-LL-PB-MF-10_R	Booster Pump(Remaining)	25	25-Jun-26 08:00	23-Jul-26 17:00	27-Aug-26 08:00 A	10-Sep-26 08:00 A	0.00	0.00	0.00	100%	100%	13
PG-H-PR-LL-PB-MF-20	GRP Sectional Panel Water Tanks (4x3x3m)(Completed)	40	05-May-26 08:00	25-Jun-26 10:00	05-May-26 08:00 A	24-Jun-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-H-PR-LL-PB-MF-20_R	GRP Sectional Panel Water Tanks (4x3x3m)(Remaining)	25	25-Jun-26 08:00	23-Jul-26 17:00	27-Aug-26 08:00 A	10-Sep-26 08:00 A	0.00	0.00	0.00	100%	100%	13
IRRIGATION WORK		107	05-May-26 08:00	08-Jul-26 17:00	05-May-26 08:00 A	10-Sep-26 08:00 A	0.00	0.00	0.00	0%	0%	-54
PG-H-PR-LL-IR-MF-10	HDPE Pipes(Completed)	40	05-May-26 08:00	25-Jun-26 10:00	05-May-26 08:00 A	24-Jun-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-H-PR-LL-IR-MF-10_R	HDPE Pipes(Remaining)	12	25-Jun-26 08:00	08-Jul-26 17:00	27-Aug-26 08:00 A	10-Sep-26 08:00 A	0.00	0.00	0.00	100%	100%	0
PG-H-PR-LL-IR-MF-20	Irrigation Control System(Completed)	40	05-May-26 08:00	25-Jun-26 10:00	05-May-26 08:00 A	24-Jun-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-H-PR-LL-IR-MF-20_R	Irrigation Control System(Remaining)	12	25-Jun-26 08:00	08-Jul-26 17:00	27-Aug-26 08:00 A	10-Sep-26 08:00 A	0.00	0.00	0.00	100%	100%	0
ELECTRICAL WORK		131	12-May-26 08:00	12-Aug-26 17:00	12-May-26 08:00 A	10-Sep-26 12:00 A	0.00	0.00	0.00	0%	0%	-25
PG-H-PR-LL-EL-MF-10	Main Distribution Board(Completed)	34	12-May-26 08:00	25-Jun-26 10:00	12-May-26 08:00 A	24-Jun-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-H-PR-LL-EL-MF-10_R	Main Distribution Board(Remaining)	13	15-Jul-26 08:00	29-Jul-26 17:00	30-Jul-26 08:00 A	10-Sep-26 12:00 A	0.00	0.00	0.00	100%	100%	-24
PG-H-PR-LL-EL-MF-20	Power Panels (Pump, Street Light)(Completed)	34	12-May-26 08:00	25-Jun-26 10:00	12-May-26 08:00 A	24-Jun-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-H-PR-LL-EL-MF-20_R	Power Panels (Pump, Street Light)(Remaining)	13	15-Jul-26 08:00	29-Jul-26 17:00	30-Jul-26 08:00 A	10-Sep-26 12:00 A	0.00	0.00	0.00	100%	100%	-24
PG-H-PR-LL-EL-MF-30	Site Lighting Poles(Completed)	34	12-May-26 08:00	25-Jun-26 10:00	12-May-26 08:00 A	24-Jun-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-H-PR-LL-EL-MF-30_R	Site Lighting Poles(Remaining)	25	15-Jul-26 08:00	12-Aug-26 17:00	30-Jul-26 08:00 A	10-Sep-26 08:00 A	0.00	0.00	0.00	100%	100%	-11
PG-H-PR-LL-EL-MF-40	Lighting Fixtures(Completed)	34	12-May-26 08:00	25-Jun-26 10:00	12-May-26 08:00 A	24-Jun-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-H-PR-LL-EL-MF-40_R	Lighting Fixtures(Remaining)	25	15-Jul-26 08:00	12-Aug-26 17:00	30-Jul-26 08:00 A	10-Sep-26 08:00 A	0.00	0.00	0.00	100%	100%	-11
PG-H-PR-LL-EL-MF-50	Grounding System Materials (Earth pit rod, LPS, etc)(Completed)	34	12-May-26 08:00	25-Jun-26 10:00	12-May-26 08:00 A	24-Jun-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-H-PR-LL-EL-MF-50_R	Grounding System Materials (Earth pit rod, LPS, etc)(Remaining)	13	23-Jul-26 08:00	06-Aug-26 17:00	27-Aug-26 08:00 A	10-Sep-26 08:00 A	0.00	0.00	0.00	100%	100%	1
PG-H-PR-LL-EL-MF-60	Telecommunications & Data System Materials (Telephone outlet, CCTV,	34	12-May-26 08:00	25-Jun-26 10:00	12-May-26 08:00 A	24-Jun-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-H-PR-LL-EL-MF-60_R	Telecommunications & Data System Materials (Telephone outlet, CCTV,	25	15-Jul-26 08:00	12-Aug-26 17:00	27-Aug-26 08:00 A	10-Sep-26 08:00 A	0.00	0.00	0.00	100%	100%	13
PG-H-PR-LL-EL-MF-70	Security and Access Control System Materials(Completed)	34	12-May-26 08:00	25-Jun-26 10:00	12-May-26 08:00 A	24-Jun-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-H-PR-LL-EL-MF-70_R	Security and Access Control System Materials(Remaining)	25	15-Jul-26 08:00	12-Aug-26 17:00	27-Aug-26 08:00 A	10-Sep-26 08:00 A	0.00	0.00	0.00	100%	100%	13
PG-H-PR-LL-EL-MF-80	Fire Alarm System Materials(Completed)	34	12-May-26 08:00	25-Jun-26 10:00	12-May-26 08:00 A	24-Jun-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-H-PR-LL-EL-MF-80_R	Fire Alarm System Materials(Remaining)	25	15-Jul-26 08:00	12-Aug-26 17:00	27-Aug-26 08:00 A	10-Sep-26 08:00 A	0.00	0.00	0.00	100%	100%	13
DELIVERY TO SITE		147	07-May-26 08:00	26-Aug-26 17:00	06-May-26 17:00 A	26-Oct-26 11:12	999,589.41	981,462.29	999,589.41	100%	98.19%	-50
EXTERNAL / LANDSCAPE WORK		118	07-May-26 08:00	06-Aug-26 17:00	06-May-26 17:00 A	15-Oct-26 17:00 A	234,716.67	234,716.67	234,716.67	100%	100%	-59
PG-H-PR-LL-LS-DL-10	Bike and Walk Path Materials(Completed)	38	07-May-26 08:00	24-Jun-26 17:00	06-May-26 17:00 A	24-Jun-26 17:00 A	103,704.30	103,704.30	103,704.30	100%	100%	0
PG-H-PR-LL-LS-DL-10_R	Bike and Walk Path Materials(Remaining)	12	25-Jul-26 08:00	06-Aug-26 17:00	06-Aug-26 08:00 A	13-Oct-26 17:00 A	44,444.70	44,444.70	44,444.70	100%	100%	-46
PG-H-PR-LL-LS-DL-20	Benches, Seats (Rectangular & Circular)(Completed)	38	07-May-26 08:00	24-Jun-26 17:00	06-May-26 17:00 A	24-Jun-26 17:00 A	28,474.61	28,474.61	28,474.61	100%	100%	0
PG-H-PR-LL-LS-DL-20_R	Benches, Seats (Rectangular & Circular)(Remaining)	12	25-Jul-26 08:00	06-Aug-26 17:00	20-Aug-26 08:00 A	15-Oct-26 17:00 A	28,474.61	28,474.61	28,474.61	100%	100%	-36
PG-H-PR-LL-LS-DL-30	Fence, gates and accessories(Completed)	38	07-May-26 08:00	24-Jun-26 17:00	06-May-26 17:00 A	24-Jun-26 17:00 A	11,847.38	11,847.38	11,847.38	100%	100%	0
PG-H-PR-LL-LS-DL-30_R	Fence, gates and accessories(Remaining)	5	01-Jul-26 08:00	06-Jul-26 17:00	22-Jul-26 08:00 A	19-Sep-26 12:00 A	17,771.08	17,771.08	17,771.08	100%	100%	-46
SPORTS & RECREATIONAL FACILITIES WORK		106	07-May-26 08:00	06-Aug-26 17:00	06-May-26 17:00 A	15-Oct-26 17:00 A	349,555.50	349,555.50	349,555.50	100%	100%	-59
PG-H-PR-LL-SP-DL-10	Football Playground Materials (Flooring, goal post, nets, paints,	38	07-May-26 08:00	24-Jun-26 17:00	06-May-26 17:00 A	24-Jun-26 17:00 A	64,212.75	64,212.75	64,212.75	100%	100%	0
PG-H-PR-LL-SP-DL-10_R	Football Playground Materials (Flooring, goal post, nets, paints,	12	25-Jul-26 08:00	06-Aug-26 17:00	06-Aug-26 08:00 A	15-Oct-26 17:00 A	64,212.75	64,212.75	64,212.75	100%	100%	-48
PG-H-PR-LL-SP-DL-20	Tartan Floor(Completed)	38	07-May-26 08:00	24-Jun-26 17:00	06-May-26 17:00 A	24-Jun-26 17:00 A	121,621.50	121,621.50	121,621.50	100%	100%	0
PG-H-PR-LL-SP-DL-20_R	Tartan Floor(Remaining)	12	25-Jul-26 08:00	06-Aug-26 17:00	06-Aug-26 08:00 A	15-Oct-26 17:00 A	99,508.50	99,508.50	99,508.50	100%	100%	-48
CONCRETE WORK		67	07-May-26 08:00	12-Jul-26 17:00	06-May-26 17:00 A	07-Jul-26 17:00 A	12,757.50	12,757.50	12,757.50	100%	100%	4
PG-H-PR-LL-CO-DL-10	Autoclaved Aerated Panel(Completed)	38	07-May-26 08:00	24-Jun-26 17:00	06-May-26 17:00 A	24-Jun-26 17:00 A	7,654.50	7,654.50	7,654.50	100%	100%	0
PG-H-PR-LL-CO-DL-10_R	Autoclaved Aerated Panel(Remaining)	5	07-Jul-26 08:00	12-Jul-26 17:00	06-Jul-26 08:00 A	07-Jul-26 17:00 A	5,103.00	5,103.00	5,103.00	100%	100%	3
METAL WORK		130	07-May-26 08:00	06-Aug-26 17:00	06-May-26 17:00 A	26-Oct-26 11:12	8,003.07	7,180.43	8,003.07	100%	89.72%	-67
PG-H-PR-LL-MT-DL-10	Metal Doors(Completed)	38	07-May-26 08:00	24-Jun-26 17:00	06-May-26 17:00 A	24-Jun-26 17:00 A	459.11	459.11	459.11	100%	100%	0
PG-H-PR-LL-MT-DL-10_R	Metal Doors(Remaining)	12	25-Jul-26 08:00	06-Aug-26 17:00	27-Aug-26 08:00 A	15-Oct-26 17:00 A	688.66	688.66	688.66	100%	100%	-30
PG-H-PR-LL-MT-DL-20	Curtain Wall(Completed)	38	07-May-26 08:00	24-Jun-26 17:00	06-May-26 17:00 A	24-Jun-26 17:00 A	2,742.12	2,742.12	2,742.12	100%	100%	0
PG-H-PR-LL-MT-DL-20_R	Curtain Wall(Remaining)	12	25-Jul-26 08:00	06-Aug-26 17:00	27-Aug-26 08:00 A	26-Oct-26 11:12	4,113.18	3,290.54	4,113.18	100%	80%	-38
PLUMBING WORK		130	07-May-26 08:00	06-Aug-26 17:00	06-May-26 17:00 A	15-Oct-26 17:00 A	31,985.55	31,985.55	31,985.55	100%	100%	-59
PG-H-PR-LL-PB-DL-10	Booster Pump(Completed)	38	07-May-26 08:00	24-Jun-26 17:00	06-May-26 17:00 A	24-Jun-26 17:00 A	6,545.88	6,545.88	6,545.88	100%	100%	0
PG-H-PR-LL-PB-DL-10_R	Booster Pump(Remaining)	12	25-Jul-26 08:00	06-Aug-26 17:00	27-Aug-26 08:00 A	21-Sep-26 17:00 A	9,818.82	9,818.82	9,818.82	100%	100%	-10
PG-H-PR-LL-PB-DL-20	GRP Sectional Panel Water Tanks (4x3x3m)(Completed)	38	07-May-26 08:00	24-Jun-26 17:00	06-May-26 17:00 A	24-Jun-26 17:00 A	6,248.34	6,248.34	6,248.34	100%	100%	0
PG-H-PR-LL-PB-DL-20_R	GRP Sectional Panel Water Tanks (4x3x3m)(Remaining)	12	25-Jul-26 08:00	06-Aug-26 17:00	27-Aug-26 08:00 A	15-Oct-26 17:00 A	9,372.51	9,372.51	9,372.51	100%	100%	-30
IRRIGATION WORK		108	07-May-26 08:00	18-Jul-26 17:00	06-May-26 17:00 A	04-Sep-26 12:48 A	115,364.25	115,364.25	115,364.25	100%	100%	-41
PG-H-PR-LL-IR-DL-10	HDPE Pipes(Completed)	38	07-May-26 08:00	24-Jun-26 17:00	06-May-26 17:00 A	24-Jun-26 17:00 A	37,226.25	37,226.25	37,226.25	100%	100%	0
PG-H-PR-LL-IR-DL-10_R	HDPE Pipes(Remaining)	8	09-Jul-26 08:00	18-Jul-26 17:00	20-Aug-26 08:00 A	27-Aug-26 17:00 A	37,226.25	37,226.25	37,226.25	100%	100%	1
PG-H-PR-LL-IR-DL-20	Irrigation Control System(Completed)	38	07-May-26 08:00	24-Jun-26 17:00	06-May-26 17:00 A	24-Jun-26 17:00 A	16,364.70	16,364.70	16,364.70	100%	100%	0
PG-H-PR-LL-IR-DL-20_R	Irrigation Control System(Remaining)	8	09-Jul-26 08:00	18-Jul-26 17:00	20-Aug-26 08:00 A	04-Sep-26 12:48 A	24,547.05	24,547.05	24,547.05	100%	100%	-5
ELECTRICAL WORK		142	13-May-26 08:00	26-Aug-26 17:00	13-May-26 08:00 A	25-Oct-26 09:36	247,206.87	229,902.39	247,206.87	100%	93%	-49
PG-H-PR-LL-EL-DL-10	Main Distribution Board(Completed)	33	13-May-26 08:00	24-Jun-26 17:00	13-May-26 08:00 A	24-Jun-26 17:00 A	1,338.93	1,338.93	1,338.93	100%	100%	0
PG-H-PR-LL-EL-DL-10_R	Main Distribution Board(Remaining)	8	30-Jul-26 08:00	08-Aug-26 17:00	27-Aug-26 08:00 A	24-Oct-26 15:24	3,124.17	2,811.75	3,124.17	100%	90%	-41
PG-H-PR-LL-EL-DL-20	Power Panels (Pump, Street Light)(Completed)	33	13-May-26 08:00	24-Jun-26 17:00	13-May-26 08:00 A	24-Jun-26 17:00 A	1,071.14	1,071.14	1,071.14	100%	100%	0
PG-H-PR-LL-EL-DL-20_R	Power Panels (Pump, Street Light)(Remaining)	8	30-Jul-26 08:00	08-Aug-26 17:00	27-Aug-26 08:00 A	24-Oct-26 15:24	2,499.34	2,249.40	2,499.34	100%	90%	-41
PG-H-PR-LL-EL-DL-30	Site Lighting Poles(Completed)	33	13-May-26 08:00	24-Jun-26 17:00	13-May-26 08:00 A	24-Jun-26 17:00 A	57,437.42	57,437.42	57,437.42	100%	100%	0
PG-H-PR-LL-EL-DL-30_R	Site Lighting Poles(Remaining)	12	13-Aug-26 08:00	26-Aug-26 17:00	20-Aug-26 08:00 A	25-Oct-26 09:36	134,020.66	120,618.59	134,020.66	100%	90%	-43
PG-H-PR-LL-EL-DL-40	Lighting Fixtures(Completed)	33	13-May-26 08:00	24-Jun-26 17:00	13-May-26 08:00 A	24-Jun-26 17:00 A	3,463.64	3,463.64	3,463.64	100%	100%	0
PG-H-PR-LL-EL-DL-40_R	Lighting Fixtures(Remaining)	12	13-Aug-26 08:00	26-Aug-26 17:00	20-Aug-26 08:00 A	25-Oct-26 09:36	8,081.83	7,273.65	8,081.83	100%	90%	-43
PG-H-PR-LL-EL-DL-50	Grounding System Materials (Earth pit rod, LPS, etc)(Completed)	33	13-May-26 08:00	24-Jun-26 17:00	13-May-26 08:00 A	24-Jun-26 17:00 A	2,711.31	2,711.31	2,711.31	100%	100%	0
PG-H-PR-LL-EL-DL-50_R	Grounding System Materials (Earth pit rod, LPS, etc)(Remaining)	8	08-Aug-26 08:00	16-Aug-26 17:00	27-Aug-26 08:00 A	24-Oct-26 15:24	6,326.40	5,693.76	6,326.40	100%	90%	-41
PG-H-PR-LL-EL-DL-60	Telecommunications & Data System Materials (Telephone outlet, CCTV,	33	13-May-26 08:00	24-Jun-26 17:00	13-May-26 08:00 A	24-Jun-26 17:00 A	2,644.33	2,644.33	2,644.33	100%	100%	0
PG-H-PR-LL-EL-DL-60_R	Telecommunications & Data System Materials (Telephone outlet, CCTV,	12	13-Aug-26 08:00	26-Aug-26 17:00	27-Aug-26 08:00 A	25-Oct-26 09:36	6,170.09	5,553.08	6,170.09	100%	90%	-37
PG-H-PR-LL-EL-DL-70	Security and Access Control System Materials(Completed)	33	13-May-26 08:00	24-Jun-26 17:00	13-May-26 08:00 A	24-Jun-26 17:00 A	3,347.73	3,347.73	3,347.73	100%	100%	0

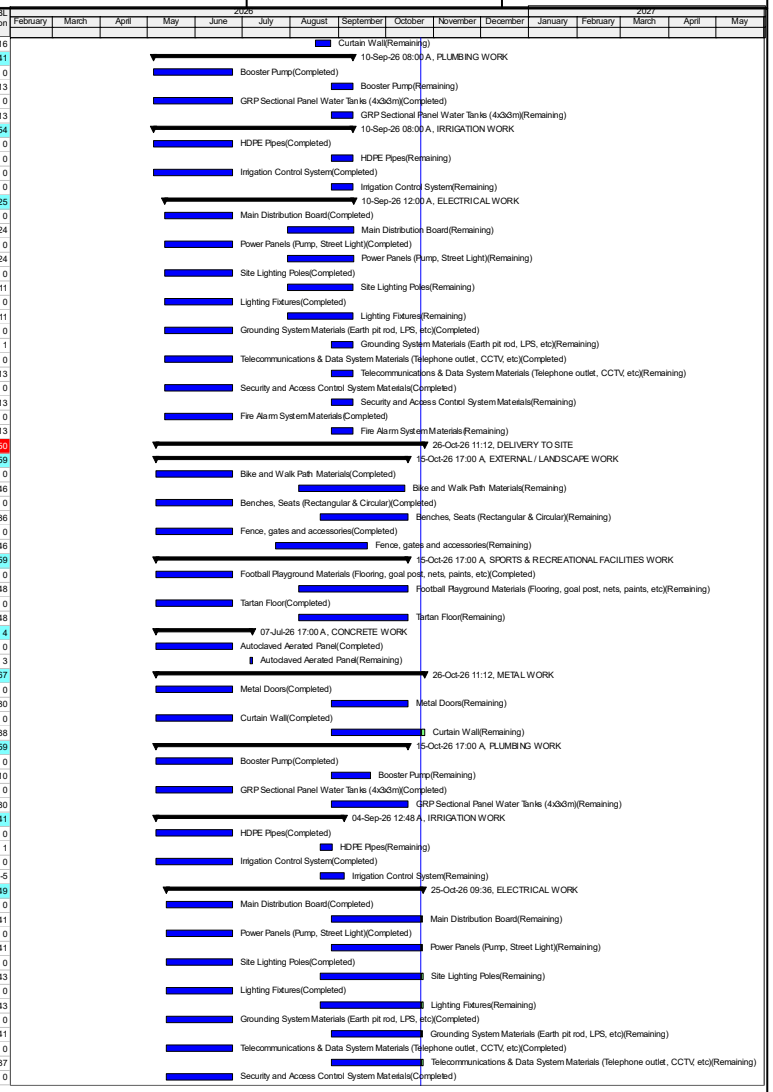


Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining W...
Milestone
summary

Baseline Schedule Rev.00

PLAYGROUNDS INITIATIVE - QASSIM, HAIL & TABUK - 25-Oct-2026

Activity ID	Activity Name	O.D	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Schedule % Complete	Performance % Complete	Variance - BL Project Duration
PG-H-PR-LL-EL-DL-70_R	Security and Access Control System Materials(Remaining)	12	13-Aug-26 08:00	26-Aug-26 17:00	27-Aug-26 08:00 A	25-Oct-26 09:36	7,811.37	7,030.23	7,811.37	100%	90%	-37
PG-H-PR-LL-EL-DL-80	Fire Alarm System Materials(Completed)	33	13-May-26 08:00	24-Jun-26 17:00	13-May-26 08:00 A	24-Jun-26 17:00 A	2,147.55	2,147.55	2,147.55	100%	100%	0
PG-H-PR-LL-EL-DL-80_R	Fire Alarm System Materials(Remaining)	12	13-Aug-26 08:00	26-Aug-26 17:00	27-Aug-26 08:00 A	25-Oct-26 09:36	5,010.96	4,509.86	5,010.96	100%	90%	-37
SHORT LEAD ITEMS		196	26-Feb-26 08:00	16-Jul-26 17:00	26-Feb-26 08:00 A	25-Oct-26 09:36	840,366.63	834,740.53	840,366.63	100%	99.33%	-84
PURCHASE ORDER		156	26-Feb-26 08:00	02-Jul-26 17:00	26-Feb-26 08:00 A	27-Aug-26 17:00 A	0.00	0.00	0.00	0%	0%	-48
EXTERNAL / LANDSCAPE WORK		156	26-Feb-26 08:00	02-Jul-26 17:00	26-Feb-26 08:00 A	27-Aug-26 17:00 A	0.00	0.00	0.00	0%	0%	-48
PG-H-PR-SL-LS-PO-10	Backfilling Materials	44	26-Feb-26 08:00	23-Apr-26 10:00	26-Feb-26 08:00 A	22-Apr-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-H-PR-SL-LS-PO-20	Interlock tiles	27	30-Mar-26 08:00	30-Apr-26 10:00	30-Mar-26 08:00 A	29-Apr-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-H-PR-SL-LS-PO-30	Compacted Natural Ground Soil	42	01-Mar-26 08:00	23-Apr-26 10:00	01-Mar-26 08:00 A	22-Apr-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-H-PR-SL-LS-PO-40	Curb Stone	22	05-Apr-26 08:00	30-Apr-26 10:00	05-Apr-26 08:00 A	29-Apr-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-H-PR-SL-LS-PO-50	Thermoplastic pavement road marking(Completed)	36	10-May-26 08:00	25-Jun-26 10:00	10-May-26 08:00 A	24-Jun-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-H-PR-SL-LS-PO-50_R	Thermoplastic pavement road marking(Remaining)	7	25-Jun-26 08:00	02-Jul-26 17:00	20-Aug-26 08:00 A	27-Aug-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-H-PR-SL-LS-PO-60	Traffic Signages(Completed)	36	10-May-26 08:00	25-Jun-26 10:00	10-May-26 08:00 A	24-Jun-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-H-PR-SL-LS-PO-60_R	Traffic Signages(Remaining)	7	25-Jun-26 08:00	02-Jul-26 17:00	20-Aug-26 08:00 A	27-Aug-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-H-PR-SL-LS-PO-70	Trees(Completed)	36	10-May-26 08:00	25-Jun-26 10:00	10-May-26 08:00 A	24-Jun-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-H-PR-SL-LS-PO-70_R	Trees(Remaining)	7	25-Jun-26 08:00	02-Jul-26 17:00	20-Aug-26 08:00 A	27-Aug-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-H-PR-SL-LS-PO-80	Lawn(Completed)	36	10-May-26 08:00	25-Jun-26 10:00	10-May-26 08:00 A	24-Jun-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-H-PR-SL-LS-PO-80_R	Lawn(Remaining)	7	25-Jun-26 08:00	02-Jul-26 17:00	20-Aug-26 08:00 A	27-Aug-26 17:00 A	0.00	0.00	0.00	100%	100%	0
CONCRETE WORK		41	02-Mar-26 08:00	23-Apr-26 10:00	02-Mar-26 08:00 A	22-Apr-26 17:00 A	0.00	0.00	0.00	0%	0%	0
PG-H-PR-SL-CO-PO-10	Steel Rebar	41	02-Mar-26 08:00	23-Apr-26 10:00	02-Mar-26 08:00 A	22-Apr-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-H-PR-SL-CO-PO-20	Concrete	36	08-Mar-26 08:00	23-Apr-26 10:00	08-Mar-26 08:00 A	22-Apr-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-H-PR-SL-CO-PO-30	Screed	23	28-Mar-26 08:00	23-Apr-26 10:00	28-Mar-26 08:00 A	22-Apr-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-H-PR-SL-CO-PO-40	CMU Block	33	11-Mar-26 08:00	23-Apr-26 10:00	11-Mar-26 08:00 A	22-Apr-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-H-PR-SL-CO-PO-50	Concrete Repair & Protection Materials	32	12-Mar-26 08:00	23-Apr-26 10:00	12-Mar-26 08:00 A	22-Apr-26 17:00 A	0.00	0.00	0.00	100%	100%	0
ARCHITECTURAL & FINISHES WORK		7	05-May-26 08:00	13-May-26 10:00	05-May-26 08:00 A	12-May-26 17:00 A	0.00	0.00	0.00	0%	0%	0
PG-H-PR-SL-AR-PO-10	Ceramic tiles	7	05-May-26 08:00	13-May-26 10:00	05-May-26 08:00 A	12-May-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-H-PR-SL-AR-PO-100	Gypsum Boards	7	05-May-26 08:00	13-May-26 10:00	05-May-26 08:00 A	12-May-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-H-PR-SL-AR-PO-110	Specialities Materials (Toilet accessories, lockers, logo, etc)	7	05-May-26 08:00	13-May-26 10:00	05-May-26 08:00 A	12-May-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-H-PR-SL-AR-PO-120	Waterproofing System Materials	7	05-May-26 08:00	13-May-26 10:00	05-May-26 08:00 A	12-May-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-H-PR-SL-AR-PO-20	Anti-slip Granite tiles	7	05-May-26 08:00	13-May-26 10:00	05-May-26 08:00 A	12-May-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-H-PR-SL-AR-PO-30	Epoxy Paint	7	05-May-26 08:00	13-May-26 10:00	05-May-26 08:00 A	12-May-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-H-PR-SL-AR-PO-40	Cement Plaster	7	05-May-26 08:00	13-May-26 10:00	05-May-26 08:00 A	12-May-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-H-PR-SL-AR-PO-50	Acrylic Paint	7	05-May-26 08:00	13-May-26 10:00	05-May-26 08:00 A	12-May-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-H-PR-SL-AR-PO-60	Stone Cladding	7	05-May-26 08:00	13-May-26 10:00	05-May-26 08:00 A	12-May-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-H-PR-SL-AR-PO-70	Aluminum Plates	7	05-May-26 08:00	13-May-26 10:00	05-May-26 08:00 A	12-May-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-H-PR-SL-AR-PO-80	Phenolic Partition	7	05-May-26 08:00	13-May-26 10:00	05-May-26 08:00 A	12-May-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-H-PR-SL-AR-PO-90	Glass Partition	7	05-May-26 08:00	13-May-26 10:00	05-May-26 08:00 A	12-May-26 17:00 A	0.00	0.00	0.00	100%	100%	0
METAL WORK		7	05-May-26 08:00	13-May-26 10:00	05-May-26 08:00 A	12-May-26 17:00 A	0.00	0.00	0.00	0%	0%	0
PG-H-PR-SL-MT-PO-10	Galvanized Steel Ladder	7	05-May-26 08:00	13-May-26 10:00	05-May-26 08:00 A	12-May-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-H-PR-SL-MT-PO-20	Galvanized Steel Roof Scupper	7	05-May-26 08:00	13-May-26 10:00	05-May-26 08:00 A	12-May-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-H-PR-SL-MT-PO-30	Galvanized Steel Cover with frame	7	05-May-26 08:00	13-May-26 10:00	05-May-26 08:00 A	12-May-26 17:00 A	0.00	0.00	0.00	100%	100%	0
HVAC WORK		7	05-May-26 08:00	13-May-26 10:00	05-May-26 08:00 A	12-May-26 17:00 A	0.00	0.00	0.00	0%	0%	0
PG-H-PR-SL-AC-PO-10	Split Air Conditioning Unit	7	05-May-26 08:00	13-May-26 10:00	05-May-26 08:00 A	12-May-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-H-PR-SL-AC-PO-20	Air Duct	7	05-May-26 08:00	13-May-26 10:00	05-May-26 08:00 A	12-May-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-H-PR-SL-AC-PO-30	Diffusers and Grills	7	05-May-26 08:00	13-May-26 10:00	05-May-26 08:00 A	12-May-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-H-PR-SL-AC-PO-40	Exhaust fans	7	05-May-26 08:00	13-May-26 10:00	05-May-26 08:00 A	12-May-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PLUMBING WORK		7	05-May-26 08:00	13-May-26 10:00	05-May-26 08:00 A	12-May-26 17:00 A	0.00	0.00	0.00	0%	0%	0
PG-H-PR-SL-PB-PO-10	PPR Pipes & Valves	7	05-May-26 08:00	13-May-26 10:00	05-May-26 08:00 A	12-May-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-H-PR-SL-PB-PO-20	UPCV Pipes	7	05-May-26 08:00	13-May-26 10:00	05-May-26 08:00 A	12-May-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-H-PR-SL-PB-PO-30	Sanitary Drainage Fixtures	7	05-May-26 08:00	13-May-26 10:00	05-May-26 08:00 A	12-May-26 17:00 A	0.00	0.00	0.00	100%	100%	0
IRRIGATION WORK		102	05-May-26 08:00	02-Jul-26 17:00	05-May-26 08:00 A	27-Aug-26 17:00 A	0.00	0.00	0.00	0%	0%	-48
PG-H-PR-SL-IR-PO-10	Gate Valve including valve box(Completed)	40	05-May-26 08:00	25-Jun-26 10:00	05-May-26 08:00 A	24-Jun-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-H-PR-SL-IR-PO-10_R	Gate Valve including valve box(Remaining)	7	25-Jun-26 08:00	02-Jul-26 17:00	20-Aug-26 08:00 A	27-Aug-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-H-PR-SL-IR-PO-20	Bubblers and Spreyers(Completed)	40	05-May-26 08:00	25-Jun-26 10:00	05-May-26 08:00 A	24-Jun-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-H-PR-SL-IR-PO-20_R	Bubblers and Spreyers(Remaining)	7	25-Jun-26 08:00	02-Jul-26 17:00	20-Aug-26 08:00 A	27-Aug-26 17:00 A	0.00	0.00	0.00	100%	100%	0
ELECTRICAL WORK		96	12-May-26 08:00	02-Jul-26 17:00	12-May-26 08:00 A	27-Aug-26 17:00 A	0.00	0.00	0.00	0%	0%	-48
PG-H-PR-SL-EL-PO-10	Wiring Devices Materials(Completed)	34	12-May-26 08:00	25-Jun-26 10:00	12-May-26 08:00 A	24-Jun-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-H-PR-SL-EL-PO-10_R	Wiring Devices Materials(Remaining)	7	25-Jun-26 08:00	02-Jul-26 17:00	27-Aug-26 08:00 A	27-Aug-26 17:00 A	0.00	0.00	0.00	100%	100%	6
FIRE FIGHTING WORK		96	12-May-26 08:00	02-Jul-26 17:00	12-May-26 08:00 A	27-Aug-26 17:00 A	0.00	0.00	0.00	0%	0%	-48
PG-H-PR-SL-FF-PO-10	Fire Extinguishers(Completed)	34	12-May-26 08:00	25-Jun-26 10:00	12-May-26 08:00 A	24-Jun-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-H-PR-SL-FF-PO-10_R	Fire Extinguishers(Remaining)	7	25-Jun-26 08:00	02-Jul-26 17:00	20-Aug-26 08:00 A	27-Aug-26 17:00 A	0.00	0.00	0.00	100%	100%	0
DELIVERY TO SITE		194	01-Mar-26 08:00	16-Jul-26 17:00	01-Mar-26 08:00 A	25-Oct-26 09:36	840,366.63	834,740.53	840,366.63	100%	99.33%	-84
EXTERNAL / LANDSCAPE WORK		166	01-Mar-26 08:00	16-Jul-26 17:00	01-Mar-26 08:00 A	25-Oct-26 09:36	649,200.96	643,574.86	649,200.96	100%	99.13%	-84
PG-H-PR-SL-LS-DL-10	Backfilling Materials	43	01-Mar-26 08:00	23-Apr-26 17:00	01-Mar-26 08:00 A	24-Apr-26 17:00 A	176,175.00	176,175.00	176,175.00	100%	100%	0
PG-H-PR-SL-LS-DL-20	Interlock tiles	12	30-Apr-26 08:00	13-May-26 17:00	30-Apr-26 08:00 A	13-May-26 17:00 A	157,450.50	157,450.50	157,450.50	100%	100%	0
PG-H-PR-SL-LS-DL-30	Compacted Natural Ground Soil	41	03-Mar-26 08:00	23-Apr-26 17:00	03-Mar-26 08:00 A	24-Apr-26 17:00 A	28,080.00	28,080.00	28,080.00	100%	100%	0
PG-H-PR-SL-LS-DL-40	Curb Stone	12	30-Apr-26 08:00	13-May-26 17:00	30-Apr-26 08:00 A	13-May-26 17:00 A	188,352.00	188,352.00	188,352.00	100%	100%	0
PG-H-PR-SL-LS-DL-50	Thermoplastic pavement road marking(Completed)	33	13-May-26 08:00	24-Jun-26 17:00	13-May-26 08:00 A	24-Jun-26 17:00 A	1,419.20	1,419.20	1,419.20	100%	100%	0
PG-H-PR-SL-LS-DL-50_R	Thermoplastic pavement road marking(Remaining)	12	04-Jul-26 08:00	16-Jul-26 17:00	27-Aug-26 08:00 A	19-Sep-26 17:00 A	3,311.47	3,311.47	3,311.47	100%	100%	-8
PG-H-PR-SL-LS-DL-60	Traffic Signages(Completed)	33	13-May-26 08:00	24-Jun-26 17:00	13-May-26 08:00 A	24-Jun-26 17:00 A	535.57	535.57	535.57	100%	100%	0
PG-H-PR-SL-LS-DL-60_R	Traffic Signages(Remaining)	12	04-Jul-26 08:00	16-Jul-26 17:00	27-Aug-26 08:00 A	25-Oct-26 09:36	1,249.67	1,124.70	1,249.67	100%	90%	-37
PG-H-PR-SL-LS-DL-70	Trees(Completed)	33	13-May-26 08:00	24-Jun-26 17:00	13-May-26 08:00 A	24-Jun-26 17:00 A	13,046.27	13,046.27	13,046.27	100%	100%	0
PG-H-PR-SL-LS-DL-70_R	Trees(Remaining)	12	04-Jul-26 08:00	16-Jul-26 17:00	27-Aug-26 08:00 A	25-Oct-26 09:36	30,441.29	27,397.16	30,441.29	100%	90%	-37

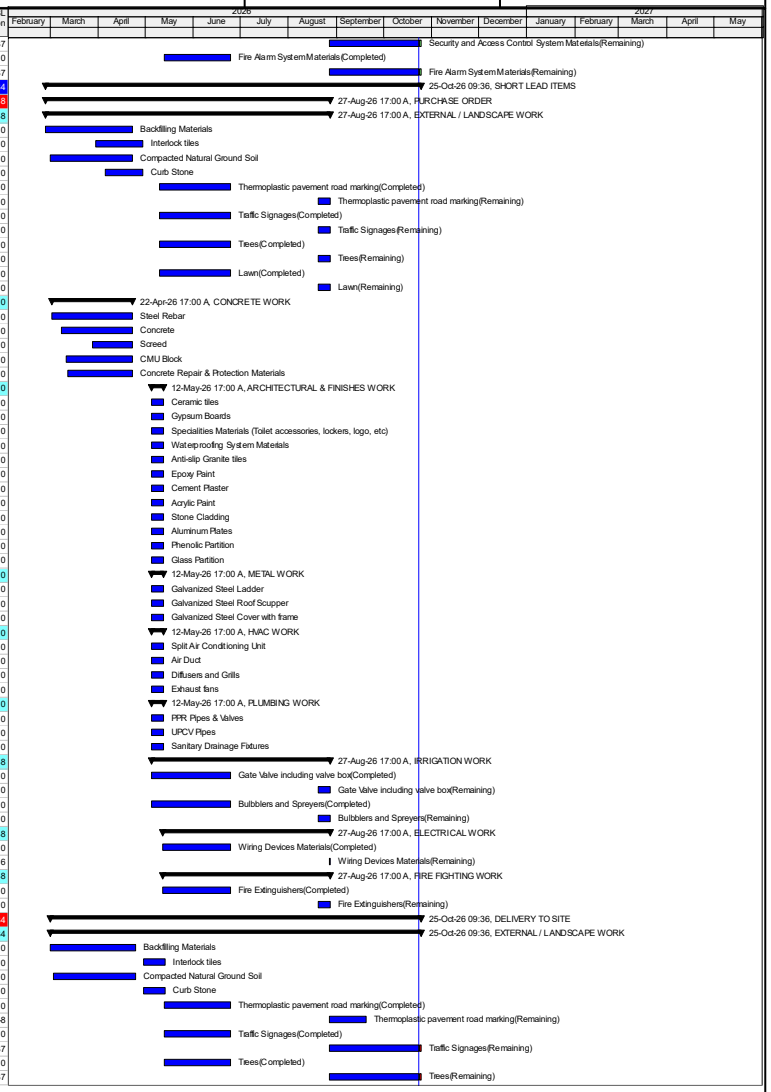

Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining W...
Milestone
summary

Baseline Schedule Rev.00

PLAYGROUNDS INITIATIVE - QASSIM, HAIL & TABUK - 25-Oct-2026

Activity ID	Activity Name	O.D	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Schedule % Complete	Performance % Complete	Variance - BL Project Duration
PG-H-PR-SL-LS-DL-80	Lawn(Completed)	33	13-May-26 08:00	24-Jun-26 17:00	13-May-26 08:00 A	24-Jun-26 17:00 A	24,570.00	24,570.00	24,570.00	100%	100%	0
PG-H-PR-SL-LS-DL-80_R	Lawn(Remaining)	12	04-Jul-26 08:00	16-Jul-26 17:00	27-Aug-26 08:00 A	25-Oct-26 09:36	24,570.00	22,113.00	24,570.00	100%	90%	-37
CONCRETE WORK		52	10-Mar-26 08:00	13-May-26 17:00	10-Mar-26 08:00 A	13-May-26 17:00 A	14,485.23	14,485.23	14,485.23	100%	100%	0
PG-H-PR-SL-CO-DL-10	Steel Rebar	12	23-Apr-26 08:00	06-May-26 17:00	23-Apr-26 08:00 A	06-May-26 17:00 A	4,291.38	4,291.38	4,291.38	100%	100%	0
PG-H-PR-SL-CO-DL-20	Concrete	35	10-Mar-26 08:00	23-Apr-26 17:00	10-Mar-26 08:00 A	24-Apr-26 17:00 A	4,669.65	4,669.65	4,669.65	100%	100%	0
PG-H-PR-SL-CO-DL-30	Screed	18	23-Apr-26 08:00	13-May-26 17:00	23-Apr-26 08:00 A	13-May-26 17:00 A	1,058.40	1,058.40	1,058.40	100%	100%	0
PG-H-PR-SL-CO-DL-40	CMU Block	18	23-Apr-26 08:00	13-May-26 17:00	23-Apr-26 08:00 A	13-May-26 17:00 A	1,117.80	1,117.80	1,117.80	100%	100%	0
PG-H-PR-SL-CO-DL-50	Concrete Repair & Protection Materials	18	23-Apr-26 08:00	13-May-26 17:00	23-Apr-26 08:00 A	13-May-26 17:00 A	3,348.00	3,348.00	3,348.00	100%	100%	0
ARCHITECTURAL & FINISHES WORK		6	06-May-26 08:00	12-May-26 17:00	06-May-26 08:00 A	12-May-26 17:00 A	73,026.09	73,026.09	73,026.09	100%	100%	0
PG-H-PR-SL-AR-DL-10	Ceramic tiles	6	06-May-26 08:00	12-May-26 17:00	06-May-26 08:00 A	12-May-26 17:00 A	5,147.55	5,147.55	5,147.55	100%	100%	0
PG-H-PR-SL-AR-DL-100	Gypsum Boards	6	06-May-26 08:00	12-May-26 17:00	06-May-26 08:00 A	12-May-26 17:00 A	1,697.22	1,697.22	1,697.22	100%	100%	0
PG-H-PR-SL-AR-DL-110	Specialities Materials (Toilet accessories, lockers, logo, etc)	6	06-May-26 08:00	12-May-26 17:00	06-May-26 08:00 A	12-May-26 17:00 A	20,365.83	20,365.83	20,365.83	100%	100%	0
PG-H-PR-SL-AR-DL-120	Waterproofing System Materials	6	06-May-26 08:00	12-May-26 17:00	06-May-26 08:00 A	12-May-26 17:00 A	4,897.80	4,897.80	4,897.80	100%	100%	0
PG-H-PR-SL-AR-DL-20	Anti-slip Granite tiles	6	06-May-26 08:00	12-May-26 17:00	06-May-26 08:00 A	12-May-26 17:00 A	4,819.50	4,819.50	4,819.50	100%	100%	0
PG-H-PR-SL-AR-DL-30	Epoxy Paint	6	06-May-26 08:00	12-May-26 17:00	06-May-26 08:00 A	12-May-26 17:00 A	1,000.62	1,000.62	1,000.62	100%	100%	0
PG-H-PR-SL-AR-DL-40	Cement Plaster	6	06-May-26 08:00	12-May-26 17:00	06-May-26 08:00 A	12-May-26 17:00 A	1,992.33	1,992.33	1,992.33	100%	100%	0
PG-H-PR-SL-AR-DL-50	Acrylic Paint	6	06-May-26 08:00	12-May-26 17:00	06-May-26 08:00 A	12-May-26 17:00 A	1,331.10	1,331.10	1,331.10	100%	100%	0
PG-H-PR-SL-AR-DL-60	Stone Cladding	6	06-May-26 08:00	12-May-26 17:00	06-May-26 08:00 A	12-May-26 17:00 A	16,669.80	16,669.80	16,669.80	100%	100%	0
PG-H-PR-SL-AR-DL-70	Aluminum Plates	6	06-May-26 08:00	12-May-26 17:00	06-May-26 08:00 A	12-May-26 17:00 A	1,642.14	1,642.14	1,642.14	100%	100%	0
PG-H-PR-SL-AR-DL-80	Phenolic Partition	6	06-May-26 08:00	12-May-26 17:00	06-May-26 08:00 A	12-May-26 17:00 A	12,063.60	12,063.60	12,063.60	100%	100%	0
PG-H-PR-SL-AR-DL-90	Glass Partition	6	06-May-26 08:00	12-May-26 17:00	06-May-26 08:00 A	12-May-26 17:00 A	1,398.60	1,398.60	1,398.60	100%	100%	0
METAL WORK		6	06-May-26 08:00	12-May-26 17:00	06-May-26 08:00 A	12-May-26 17:00 A	4,310.01	4,310.01	4,310.01	100%	100%	0
PG-H-PR-SL-MT-DL-10	Galvanized Steel Ladder	6	06-May-26 08:00	12-May-26 17:00	06-May-26 08:00 A	12-May-26 17:00 A	3,256.74	3,256.74	3,256.74	100%	100%	0
PG-H-PR-SL-MT-DL-20	Galvanized Steel Roof Scupper	6	06-May-26 08:00	12-May-26 17:00	06-May-26 08:00 A	12-May-26 17:00 A	281.88	281.88	281.88	100%	100%	0
PG-H-PR-SL-MT-DL-30	Galvanized Steel Cover with frame	6	06-May-26 08:00	12-May-26 17:00	06-May-26 08:00 A	12-May-26 17:00 A	771.39	771.39	771.39	100%	100%	0
HVAC WORK		6	06-May-26 08:00	12-May-26 17:00	06-May-26 08:00 A	12-May-26 17:00 A	5,457.24	5,457.24	5,457.24	100%	100%	0
PG-H-PR-SL-AC-DL-10	Split Air Conditioning Unit	6	06-May-26 08:00	12-May-26 17:00	06-May-26 08:00 A	12-May-26 17:00 A	2,789.37	2,789.37	2,789.37	100%	100%	0
PG-H-PR-SL-AC-DL-20	Air Duct	6	06-May-26 08:00	12-May-26 17:00	06-May-26 08:00 A	12-May-26 17:00 A	1,404.00	1,404.00	1,404.00	100%	100%	0
PG-H-PR-SL-AC-DL-30	Diffusers and Grills	6	06-May-26 08:00	12-May-26 17:00	06-May-26 08:00 A	12-May-26 17:00 A	668.79	668.79	668.79	100%	100%	0
PG-H-PR-SL-AC-DL-40	Exhaust fans	6	06-May-26 08:00	12-May-26 17:00	06-May-26 08:00 A	12-May-26 17:00 A	595.08	595.08	595.08	100%	100%	0
PLUMBING WORK		6	06-May-26 08:00	12-May-26 17:00	06-May-26 08:00 A	12-May-26 17:00 A	28,323.27	28,323.27	28,323.27	100%	100%	0
PG-H-PR-SL-PB-DL-10	PPR Pipes & Valves	6	06-May-26 08:00	12-May-26 17:00	06-May-26 08:00 A	12-May-26 17:00 A	2,386.80	2,386.80	2,386.80	100%	100%	0
PG-H-PR-SL-PB-DL-20	UPCV Pipes	6	06-May-26 08:00	12-May-26 17:00	06-May-26 08:00 A	12-May-26 17:00 A	3,016.71	3,016.71	3,016.71	100%	100%	0
PG-H-PR-SL-PB-DL-30	Sanitary Drainage Fixtures	6	06-May-26 08:00	12-May-26 17:00	06-May-26 08:00 A	12-May-26 17:00 A	22,919.76	22,919.76	22,919.76	100%	100%	0
IRRIGATION WORK		113	06-May-26 08:00	16-Jul-26 17:00	06-May-26 08:00 A	15-Oct-26 17:00 A	61,691.76	61,691.76	61,691.76	100%	100%	-77
PG-H-PR-SL-IR-DL-10	Gate Valve including valve box(Completed)	39	06-May-26 08:00	24-Jun-26 17:00	06-May-26 08:00 A	24-Jun-26 17:00 A	3,403.35	3,403.35	3,403.35	100%	100%	0
PG-H-PR-SL-IR-DL-10_R	Gate Valve including valve box(Remaining)	12	04-Jul-26 08:00	16-Jul-26 17:00	20-Aug-26 08:00 A	15-Oct-26 17:00 A	3,403.35	3,403.35	3,403.35	100%	100%	-36
PG-H-PR-SL-IR-DL-20	Bubblers and Spreyers(Completed)	39	06-May-26 08:00	24-Jun-26 17:00	06-May-26 08:00 A	24-Jun-26 17:00 A	27,442.53	27,442.53	27,442.53	100%	100%	0
PG-H-PR-SL-IR-DL-20_R	Bubblers and Spreyers(Remaining)	12	04-Jul-26 08:00	16-Jul-26 17:00	27-Aug-26 08:00 A	15-Oct-26 17:00 A	27,442.53	27,442.53	27,442.53	100%	100%	-30
ELECTRICAL WORK		117	20-May-26 08:00	16-Jul-26 17:00	20-May-26 08:00 A	15-Oct-26 17:00 A	3,667.68	3,667.68	3,667.68	100%	100%	-77
PG-H-PR-SL-EL-DL-10	Wiring Devices Materials(Completed)	27	20-May-26 08:00	24-Jun-26 17:00	20-May-26 08:00 A	24-Jun-26 17:00 A	1,100.30	1,100.30	1,100.30	100%	100%	0
PG-H-PR-SL-EL-DL-10_R	Wiring Devices Materials(Remaining)	12	04-Jul-26 08:00	16-Jul-26 17:00	26-Sep-26 08:00 A	15-Oct-26 17:00 A	2,567.38	2,567.38	2,567.38	100%	100%	-6
FIRE FIGHTING WORK		129	20-May-26 08:00	16-Jul-26 17:00	20-May-26 08:00 A	15-Oct-26 17:00 A	204.39	204.39	204.39	100%	100%	-77
PG-H-PR-SL-FF-DL-10	Fire Extinguishers(Completed)	27	20-May-26 08:00	24-Jun-26 17:00	20-May-26 08:00 A	24-Jun-26 17:00 A	61.32	61.32	61.32	100%	100%	0
PG-H-PR-SL-FF-DL-10_R	Fire Extinguishers(Remaining)	12	04-Jul-26 08:00	16-Jul-26 17:00	03-Oct-26 08:00 A	15-Oct-26 17:00 A	143.07	143.07	143.07	100%	100%	0
CONSTRUCTION STAGE		237	05-Apr-26 08:00	25-Nov-26 17:00	05-Apr-26 08:00 A	21-Dec-26 14:36	3,941,913.75	3,560,642.09	4,088,791.20	96.41%	87.08%	-21
PLAYGROUND AND LANDSCAPING WORKS		237	05-Apr-26 08:00	26-Nov-26 17:00	05-Apr-26 08:00 A	21-Dec-26 14:36	3,813,420.17	3,286,366.22	3,760,297.62	98.09%	87.4%	-21
CUT AND FILL		28	05-Apr-26 08:00	06-May-26 17:00	05-Apr-26 08:00 A	06-May-26 17:00 A	453,900.00	453,900.00	453,900.00	100%	100%	0
PG-H-CON-EX-CF-10	Existing Soil Excavation Works	26	05-Apr-26 08:00	04-May-26 17:00	05-Apr-26 08:00 A	04-May-26 17:00 A	125,280.00	125,280.00	125,280.00	100%	100%	0
PG-H-CON-EX-CF-20	Soil Replacement Works	21	12-Apr-26 08:00	05-May-26 17:00	12-Apr-26 08:00 A	05-May-26 17:00 A	62,400.00	62,400.00	62,400.00	100%	100%	0
PG-H-CON-EX-CF-30	Levelling & Backfilling Works	18	16-Apr-26 08:00	06-May-26 17:00	16-Apr-26 08:00 A	06-May-26 17:00 A	266,220.00	266,220.00	266,220.00	100%	100%	0
PLAYGROUND WORKS		177	19-Apr-26 08:00	17-Nov-26 17:00	19-Apr-26 08:00 A	16-Nov-26 12:48	754,153.08	701,267.82	781,940.40	96.45%	89.68%	1
FOOTBALL PLAYGROUND WORKS		177	19-Apr-26 08:00	17-Nov-26 17:00	19-Apr-26 08:00 A	16-Nov-26 12:48	754,153.08	701,267.82	781,940.40	96.45%	89.68%	1
PG-H-CON-EX-FB-10	Subgrade Preparation and Compaction	16	19-Apr-26 08:00	06-May-26 17:00	19-Apr-26 08:00 A	06-May-26 17:00 A	23,667.00	23,667.00	23,667.00	100%	100%	0
PG-H-CON-EX-FB-100	Markings and Signages	10	07-Nov-26 08:00	17-Nov-26 17:00	04-Nov-26 12:48	16-Nov-26 12:48	0.00	0.00	23,667.00	0%	0%	0
PG-H-CON-EX-FB-110	Install Playground Benches	15	20-Oct-26 08:00	05-Nov-26 17:00	27-Aug-26 08:00 A	04-Nov-26 12:48	1,030.08	4,120.32	5,150.40	20%	80%	-44
PG-H-CON-EX-FB-120	Installation of Lighting System	13	18-Aug-26 08:00	01-Sep-26 17:00	27-Aug-26 08:00 A	26-Oct-26 12:48	48,720.00	38,976.00	48,720.00	100%	80%	-38
PG-H-CON-EX-FB-20	Sub-Base Laying and Compaction	12	23-Apr-26 08:00	06-May-26 17:00	23-Apr-26 08:00 A	06-May-26 17:00 A	23,667.00	23,667.00	23,667.00	100%	100%	0
PG-H-CON-EX-FB-30	Base Course Laying and Compaction	33	06-May-26 08:00	17-Jun-26 17:00	06-May-26 08:00 A	17-Jun-26 17:00 A	23,667.00	23,667.00	23,667.00	100%	100%	0
PG-H-CON-EX-FB-40	Tartan flooring(Completed)	7	17-Jun-26 08:00	24-Jun-26 17:00	17-Jun-26 08:00 A	24-Jun-26 17:00 A	147,420.00	147,420.00	147,420.00	100%	100%	0
PG-H-CON-EX-FB-40_R	Tartan flooring(Remaining)	15	16-Sep-26 08:00	04-Oct-26 17:00	06-Aug-26 08:00 A	28-Oct-26 17:00	343,980.00	309,582.00	343,980.00	100%	90%	-56
PG-H-CON-EX-FB-50	Goal Post Foundation	17	29-Jul-26 08:00	17-Aug-26 17:00	20-Aug-26 08:00 A	15-Oct-26 17:00 A	35,500.50	35,500.50	35,500.50	100%	100%	-31
PG-H-CON-EX-FB-60	Goal Post Installation & Alignment	13	05-Oct-26 08:00	19-Oct-26 17:00	20-Aug-26 08:00 A	01-Nov-26 12:48	35,500.50	28,400.40	35,500.50	100%	80%	-49
PG-H-CON-EX-FB-70	Topsoil Placement(Completed)	33	13-May-26 08:00	24-Jun-26 17:00	13-May-26 08:00 A	24-Jun-26 17:00 A	7,100.10	7,100.10	7,100.10	100%	100%	0
PG-H-CON-EX-FB-70_R	Topsoil Placement(Remaining)	14	13-Jul-26 08:00	28-Jul-26 17:00	30-Jul-26 08:00 A	14-Aug-26 17:00 A	16,566.90	16,566.90	16,566.90	100%	100%	1
PG-H-CON-EX-FB-80	Fine Grading & Leveling	15	25-Jun-26 08:00	12-Jul-26 17:00	12-Jul-26 08:00 A	14-Aug-26 17:00 A	23,667.00	23,667.00	23,667.00	100%	100%	-14
PG-H-CON-EX-FB-90	Turfing / Seeding Works	12	02-Sep-26 08:00	15-Sep-26 17:00	14-Aug-26 08:00 A	28-Oct-26 17:00	23,667.00	18,933.60	23,667.00	100%	80%	-52
GENERAL SITE WORKS		227	16-Apr-26 08:00	26-Nov-26 17:00	16-Apr-26 08:00 A	21-Dec-26 14:36	1,217,232.42	1,003,799.83	1,224,114.42	99.44%	82%	-21
FENCE WORKS		159	16-Apr-26 08:00	16-Aug-26 17:00	16-Apr-26 08:00 A	15-Oct-26 17:00 A	65,818.80	65,818.80	65,818.80	100%	100%	-51
PG-H-CON-EX-GN-FN-10	Excavation for fence foundation	3	16-Apr-26 08:00	19-Apr-26 17:00	16-Apr-26 08:00 A	19-Apr-26 17:00 A	13,163.76	13,163.76	13,163.76	100%	100%	0
PG-H-CON-EX-GN-FN-20	Concrete Foundations for Fence	9	13-Jul-26 08:00	22-Jul-26 17:00	13-Aug-26 08:00 A	20-Aug-26 17:00 A	13,163.76	13,163.76	13,163.76	100%	100%	2
PG-H-CON-EX-GN-FN-30	Installation of Galvanized Steel Posts & Framing	9	23-Jul-26 08:00	02-Aug-26 17:00	27-Aug-26 08:00 A	14-Oct-26 17:00 A	13,163.76	13,163.76	13,163.76	100%	100%	-32
PG-H-CON-EX-GN-FN-40	Fixing of Chain Link Mesh, Tensioning & Bracing	8	03-Aug-26 08:00	11-Aug-26 17:00	27-Sep-26 15:24 A	15-Oct-26 17:00 A	13,163.76	13,163.76	13,163.76	100%	100%	-8



Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining W...
Milestone
summary

Baseline Schedule Rev.00

PLAYGROUNDS INITIATIVE - QASSIM, HAIL & TABUK - 25-Oct-2026

Activity ID	Activity Name	O.D	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Schedule % Complete	Performance % Complete	Variance - BL Project Duration
PG-H-CON-EX-GN-FN-50	Installation of Gates	4	12-Aug-26 08:00	16-Aug-26 17:00	05-Oct-26 08:00 A	15-Oct-26 17:00 A	13,163.76	13,163.76	13,163.76	100%	100%	-6
MECHANICAL WORK		152	12-May-26 08:00	06-Aug-26 17:00	12-May-26 08:00 A	09-Nov-26 10:24	421,027.74	358,530.44	421,027.74	100%	85.16%	-79
STORM WATER AND UTILITY WORK		150	12-May-26 08:00	04-Aug-26 17:00	12-May-26 08:00 A	08-Nov-26 12:00	27,252.00	18,292.80	27,252.00	100%	67.12%	-81
PG-H-CON-EX-GN-M-10	Excavation	2	12-May-26 08:00	13-May-26 17:00	12-May-26 08:00 A	13-May-26 17:00 A	3,096.00	3,096.00	3,096.00	100%	100%	0
PG-H-CON-EX-GN-M-20	Bedding preparation & level control(Completed)	27	20-May-26 08:00	24-Jun-26 17:00	20-May-26 08:00 A	24-Jun-26 17:00 A	1,032.00	1,032.00	1,032.00	100%	100%	0
PG-H-CON-EX-GN-M-20_R	Bedding preparation & level control(Remaining)	10	25-Jun-26 08:00	06-Jul-26 17:00	14-Aug-26 08:00 A	24-Oct-26 17:00	1,032.00	928.80	1,032.00	100%	90%	-50
PG-H-CON-EX-GN-M-30	Manhole Installation	5	07-Jul-26 08:00	12-Jul-26 17:00	27-Aug-26 08:00 A	25-Oct-26 12:00	5,160.00	4,644.00	5,160.00	100%	90%	-45
PG-H-CON-EX-GN-M-40	150 mm uPVC pipe laying & jointing	4	13-Jul-26 08:00	16-Jul-26 17:00	13-Oct-26 08:00 A	26-Oct-26 10:24	10,740.00	8,592.00	10,740.00	100%	80%	-7
PG-H-CON-EX-GN-M-50	Concrete Encasement	3	18-Jul-26 08:00	20-Jul-26 17:00	26-Oct-26 10:24	29-Oct-26 10:24	2,064.00	0.00	2,064.00	100%	0%	0
PG-H-CON-EX-GN-M-60	Backfilling & Compaction	3	21-Jul-26 08:00	23-Jul-26 17:00	29-Oct-26 10:24	02-Nov-26 10:24	2,064.00	0.00	2,064.00	100%	0%	0
PG-H-CON-EX-GN-M-70	Surface Reinstatement & Civil Works	4	01-Aug-26 08:00	04-Aug-26 17:00	03-Nov-26 12:00	08-Nov-26 12:00	2,064.00	0.00	2,064.00	100%	0%	0
IRRIGATION SYSTEM WORKS		132	02-Jun-26 09:36	30-Jul-26 17:00	02-Jun-26 09:36 A	03-Nov-26 12:00	393,457.80	340,046.88	393,457.80	100%	86.43%	-81
PG-H-CON-EX-GN-M-100	Installation of Bubblers and Sprinklers	3	28-Jul-26 08:00	30-Jul-26 17:00	10-Oct-26 08:00 A	03-Nov-26 12:00	121,966.80	97,573.44	121,966.80	100%	80%	-19
PG-H-CON-EX-GN-M-80	Installation of HDPE Irrigation Pipe Network with Gate Valve and	20	02-Jun-26 09:36	24-Jun-26 17:00	02-Jun-26 09:36 A	24-Jun-26 17:00 A	72,230.40	72,230.40	72,230.40	100%	100%	0
PG-H-CON-EX-GN-M-80_R	Installation of HDPE Irrigation Pipe Network with Gate Valve and	2	21-Jul-26 08:00	23-Jul-26 17:00	14-Aug-26 08:00 A	02-Nov-26 10:24	108,345.60	97,511.04	108,345.60	100%	90%	-64
PG-H-CON-EX-GN-M-90	Installation of Irrigation Control System	3	25-Jul-26 08:00	27-Jul-26 17:00	26-Aug-26 08:00 A	02-Nov-26 16:12	90,915.00	72,732.00	90,915.00	100%	80%	-55
FIRE PROTECTION SYSTEM		2	05-Aug-26 08:00	06-Aug-26 17:00	11-Oct-26 08:00 A	09-Nov-26 10:24	317.94	190.76	317.94	100%	60%	-23
PG-H-CON-EX-GN-M-110	Fire Extinguisher Installation	2	05-Aug-26 08:00	06-Aug-26 17:00	11-Oct-26 08:00 A	09-Nov-26 10:24	317.94	190.76	317.94	100%	60%	-23
ELECTRICAL WORK		198	20-May-26 08:00	20-Oct-26 17:00	20-May-26 08:00 A	05-Dec-26 10:24	539,251.68	418,854.59	539,251.68	100%	77.67%	-38
POWER, LIGHTING & GROUNDING		163	20-May-26 08:00	08-Sep-26 17:00	20-May-26 08:00 A	18-Nov-26 10:24	482,181.48	384,612.47	482,181.48	100%	79.77%	-59
PG-H-CON-EX-GN-E-10	Excavation(Completed)	27	20-May-26 08:00	24-Jun-26 17:00	20-May-26 08:00 A	24-Jun-26 17:00 A	63,819.36	63,819.36	63,819.36	100%	100%	0
PG-H-CON-EX-GN-E-10_R	Excavation(Remaining)	1	04-Aug-26 08:00	04-Aug-26 17:00	16-Jul-26 08:00 A	27-Aug-26 17:00 A	63,819.36	63,819.36	63,819.36	100%	100%	-36
PG-H-CON-EX-GN-E-20	Foundation Work for Site Lighting Poles(Completed)	13	10-Jun-26 08:00	24-Jun-26 17:00	10-Jun-26 08:00 A	24-Jun-26 17:00 A	51,055.49	51,055.49	51,055.49	100%	100%	0
PG-H-CON-EX-GN-E-20_R	Foundation Work for Site Lighting Poles(Remaining)	4	05-Aug-26 08:00	09-Aug-26 17:00	20-Aug-26 08:00 A	09-Nov-26 09:36	119,129.47	95,303.58	119,129.47	100%	80%	-64
PG-H-CON-EX-GN-E-30	Lightning Protection System (LPS)	3	17-Aug-26 08:00	19-Aug-26 17:00	10-Oct-26 08:00 A	10-Nov-26 12:00	8,265.00	4,959.00	8,265.00	100%	60%	-25
PG-H-CON-EX-GN-E-40	KWH Meter and MDB Installation	2	20-Aug-26 08:00	22-Aug-26 17:00	11-Oct-26 08:00 A	11-Nov-26 10:24	4,586.70	2,752.02	4,586.70	100%	60%	-25
PG-H-CON-EX-GN-E-50	Power Panels and Distribution Boards	5	23-Aug-26 08:00	27-Aug-26 17:00	11-Oct-26 08:00 A	14-Nov-26 10:24	17,397.90	10,438.74	17,397.90	100%	60%	-24
PG-H-CON-EX-GN-E-60	Site Lighting Poles Installation	3	29-Aug-26 08:00	31-Aug-26 17:00	12-Oct-26 08:00 A	15-Nov-26 12:00	127,638.72	76,583.23	127,638.72	100%	60%	-27
PG-H-CON-EX-GN-E-70	Wiring Works	3	01-Sep-26 08:00	03-Sep-26 17:00	10-Oct-26 08:00 A	16-Nov-26 14:36	4,224.00	2,534.40	4,224.00	100%	60%	-30
PG-H-CON-EX-GN-E-80	Lighting Fixtures with outlets Installation	4	05-Sep-26 08:00	08-Sep-26 17:00	13-Oct-26 08:00 A	18-Nov-26 10:24	22,245.48	13,347.29	22,245.48	100%	60%	-27
ELV SYSTEMS (TELECOM, DATA, AV & CCTV)		25	09-Sep-26 08:00	08-Oct-26 17:00	10-Oct-26 08:00 A	30-Nov-26 10:24	43,146.00	25,887.60	43,146.00	100%	60%	-19
PG-H-CON-EX-GN-E-100	Fiber Optic Pull Box Installation	3	13-Sep-26 08:00	15-Sep-26 17:00	12-Oct-26 08:00 A	21-Nov-26 14:36	619.80	371.88	619.80	100%	60%	-32
PG-H-CON-EX-GN-E-110	Telephone and Data Outlet Installation	4	16-Sep-26 08:00	20-Sep-26 17:00	12-Oct-26 08:00 A	23-Nov-26 10:24	3,718.80	2,231.28	3,718.80	100%	60%	-32
PG-H-CON-EX-GN-E-120	Telecom Equipment and AV HDMI Installation	4	21-Sep-26 08:00	26-Sep-26 17:00	13-Oct-26 08:00 A	24-Nov-26 16:12	15,249.12	9,149.47	15,249.12	100%	60%	-33
PG-H-CON-EX-GN-E-130	CCTV Rack / Cabinet Installation	4	27-Sep-26 08:00	30-Sep-26 17:00	10-Oct-26 08:00 A	26-Nov-26 12:00	1,446.48	867.89	1,446.48	100%	60%	-38
PG-H-CON-EX-GN-E-140	NVR and CCTV Monitor Installation	4	01-Oct-26 08:00	05-Oct-26 17:00	10-Oct-26 08:00 A	29-Nov-26 08:48	6,612.00	3,967.20	6,612.00	100%	60%	-39
PG-H-CON-EX-GN-E-150	IP Camera Installation	3	06-Oct-26 08:00	08-Oct-26 17:00	10-Oct-26 08:00 A	30-Nov-26 10:24	14,880.00	8,928.00	14,880.00	100%	60%	-41
PG-H-CON-EX-GN-E-90	ELV Containment & Cabling Works	3	09-Sep-26 08:00	12-Sep-26 17:00	11-Oct-26 08:00 A	19-Nov-26 12:00	619.80	371.88	619.80	100%	60%	-32
FIRE ALARM SYSTEM		32	13-Sep-26 08:00	20-Oct-26 17:00	10-Oct-26 08:00 A	05-Dec-26 10:24	13,924.20	8,354.52	13,924.20	100%	60%	-16
PG-H-CON-EX-GN-E-160	Fire Alarm Containment & Cabling	8	13-Sep-26 08:00	21-Sep-26 17:00	10-Oct-26 08:00 A	23-Nov-26 14:36	1,983.60	1,190.16	1,983.60	100%	60%	-31
PG-H-CON-EX-GN-E-170	Fire Alarm Control Panel (FACP) Installation	8	22-Sep-26 08:00	01-Oct-26 17:00	10-Oct-26 08:00 A	26-Nov-26 16:12	2,644.80	1,586.88	2,644.80	100%	60%	-34
PG-H-CON-EX-GN-E-180	Initiating Devices (Detectors & Manual Pull Station)	8	03-Oct-26 08:00	11-Oct-26 17:00	10-Oct-26 08:00 A	01-Dec-26 08:48	8,097.60	4,858.56	8,097.60	100%	60%	-37
PG-H-CON-EX-GN-E-190	Notification Appliances (Strobe with Sounder)	8	12-Oct-26 08:00	20-Oct-26 17:00	10-Oct-26 08:00 A	05-Dec-26 10:24	1,198.20	718.92	1,198.20	100%	60%	-40
PARKING WORK		147	17-Jun-26 08:00	20-Oct-26 17:00	17-Jun-26 08:00 A	07-Dec-26 10:24	190,576.20	155,574.00	190,576.20	100%	81.63%	-40
PG-H-CON-EX-GN-PR-10	Installation of Parking Accessories	5	10-Oct-26 08:00	14-Oct-26 17:00	20-Aug-26 08:00 A	01-Dec-26 10:24	86,430.00	69,144.00	86,430.00	100%	80%	-82
PG-H-CON-EX-GN-PR-20	Interlock tiles(Completed)	7	17-Jun-26 08:00	24-Jun-26 17:00	17-Jun-26 08:00 A	24-Jun-26 17:00 A	38,893.50	38,893.50	38,893.50	100%	100%	0
PG-H-CON-EX-GN-PR-20_R	Interlock tiles(Remaining)	3	12-Oct-26 08:00	14-Oct-26 17:00	11-Jul-26 08:00 A	30-Jul-26 17:00 A	47,536.50	47,536.50	47,536.50	100%	100%	-15
PG-H-CON-EX-GN-PR-30	Marking & Signages	5	15-Oct-26 08:00	20-Oct-26 17:00	01-Dec-26 10:24	07-Dec-26 10:24	17,716.20	0.00	17,716.20	100%	0%	0
SERVICE CONNECTION		23	21-Oct-26 08:00	26-Nov-26 17:00	30-Jul-26 08:00 A	21-Dec-26 14:36	558.00	5,022.00	7,440.00	7.5%	67.5%	-91
PG-H-CON-EX-GN-SC-10	Excavation & Tiench Preparation	8	21-Oct-26 08:00	29-Oct-26 17:00	30-Jul-26 08:00 A	27-Aug-26 17:00 A	558.00	2,232.00	2,232.00	25%	100%	-17
PG-H-CON-EX-GN-SC-20	HDPE Pipe Laying & Valve Installation	8	31-Oct-26 08:00	08-Nov-26 17:00	20-Aug-26 08:00 A	08-Dec-26 12:00	0.00	1,897.20	2,232.00	0%	85%	-86
PG-H-CON-EX-GN-SC-30	Connection to City Network	8	09-Nov-26 08:00	17-Nov-26 17:00	08-Dec-26 12:00	17-Dec-26 12:00	0.00	0.00	1,488.00	0%	0%	0
PG-H-CON-EX-GN-SC-40	Backfilling	8	18-Nov-26 08:00	26-Nov-26 17:00	27-Aug-26 08:00 A	21-Dec-26 14:36	0.00	892.80	1,488.00	0%	60%	-91
LANDSCAPING WORKS		163	31-May-26 08:00	09-Nov-26 17:00	30-May-26 16:12 A	07-Dec-26 12:48	1,139,844.27	1,100,356.27	1,252,052.40	91.04%	87.88%	-24
HARDSCAPE WORK		163	31-May-26 08:00	09-Nov-26 17:00	30-May-26 16:12 A	07-Dec-26 12:48	988,605.27	1,002,076.27	1,046,213.40	94.49%	95.78%	-24
PG-H-CON-EX-LS-HS-10	Curbstone Installation(Completed)	22	31-May-26 08:00	24-Jun-26 17:00	30-May-26 16:12 A	24-Jun-26 17:00 A	251,136.00	251,136.00	251,136.00	100%	100%	0
PG-H-CON-EX-LS-HS-10_R	Curbstone Installation(Remaining)	8	10-Sep-26 08:00	19-Sep-26 17:00	22-Jul-26 08:00 A	27-Aug-26 17:00 A	167,424.00	167,424.00	167,424.00	100%	100%	-24
PG-H-CON-EX-LS-HS-20	Interlock Tiles Grey Scale with Black Marble Chips(Completed)	22	31-May-26 08:00	24-Jun-26 17:00	30-May-26 16:12 A	24-Jun-26 17:00 A	36,036.00	36,036.00	36,036.00	100%	100%	0
PG-H-CON-EX-LS-HS-20_R	Interlock Tiles Grey Scale with Black Marble Chips(Remaining)	13	20-Sep-26 08:00	05-Oct-26 17:00	27-Aug-26 08:00 A	21-Oct-26 17:00 A	54,054.00	54,054.00	54,054.00	100%	100%	-34
PG-H-CON-EX-LS-HS-30	Stamped Concrete Floor(Completed)	13	10-Jun-26 08:00	24-Jun-26 17:00	10-Jun-26 08:00 A	24-Jun-26 17:00 A	43,470.00	43,470.00	43,470.00	100%	100%	0
PG-H-CON-EX-LS-HS-30_R	Stamped Concrete Floor(Remaining)	15	20-Sep-26 08:00	07-Oct-26 17:00	30-Jul-26 08:00 A	22-Oct-26 17:00 A	43,470.00	43,470.00	43,470.00	100%	100%	-57
PG-H-CON-EX-LS-HS-40	Bike Path and Walking Path Construction(Completed)	22	31-May-26 08:00	24-Jun-26 17:00	30-May-26 16:12 A	24-Jun-26 17:00 A	181,071.00	181,071.00	181,071.00	100%	100%	0
PG-H-CON-EX-LS-HS-40_R	Bike Path and Walking Path Construction(Remaining)	8	08-Oct-26 08:00	17-Oct-26 17:00	09-Jul-26 08:00 A	22-Nov-26 17:00	148,149.00	140,741.55	148,149.00	100%	95%	-108
PG-H-CON-EX-LS-HS-50	Install Recycled Precast Concrete Seats(Completed)	22	31-May-26 08:00	24-Jun-26 17:00	30-May-26 16:12 A	24-Jun-26 17:00 A	11,599.14	11,599.14	11,599.14	100%	100%	0
PG-H-CON-EX-LS-HS-50_R	Install Recycled Precast Concrete Seats(Remaining)	10	18-Oct-26 08:00	28-Oct-26 17:00	30-Jul-26 08:00 A	25-Nov-26 12:48	52,196.13	73,074.58	104,392.26	50%	70%	-91
PG-H-CON-EX-LS-HS-60	Install Recycled Precast Concrete Trash Bins	10	29-Oct-26 08:00	09-Nov-26 17:00	25-Nov-26 12:48	07-Dec-26 12:48	0.00	0.00	5,412.00	0%	0%	0
SOFTSCAPE WORK		155	03-Jun-26 10:00	09-Nov-26 17:00	03-Jun-26 10:00 A	07-Dec-26 12:48	151,239.00	98,280.00	205,839.00	73.47%	47.75%	-24
PG-H-CON-EX-LS-SS-10	Planting Trees	10	06-Oct-26 08:00	17-Oct-26 17:00	11-Nov-26 08:00	22-Nov-26 17:00	96,639.00	0.00	96,639.00	100%	0%	0
PG-H-CON-EX-LS-SS-20	Lawn Area Preparation & Planting / Turfing(Completed)	19	03-Jun-26 10:00	24-Jun-26 17:00	03-Jun-26 10:00 A	24-Jun-26 17:00 A	54,600.00	54,600.00	54,600.00	100%	100%	0
PG-H-CON-EX-LS-SS-20_R	Lawn Area Preparation & Planting / Turfing(Remaining)	7	02-Nov-26 08:00	09-Nov-26 17:00	27-Aug-26 08:00 A	07-Dec-26 12:48	0.00	43,680.00	54,600.00	0%	80%	-80
TANK WORKS		148	13-May-26 08:00	19-Sep-26 17:00	13-May-26 08:00 A	10-Nov-26 17:00	48,290.40	27,042.30	48,290.40	100%	56%	-44
SEPTIC TANK		148	13-May-26 08:00	31-Aug-26 17:00	13-May-26 08:00 A	07-Nov-26 17:00	7,475.22	7,054.92	7,475.22	100%	94.38%	-57
PG-H-CON-EX-TW-ST-10	Excavation	32	13-May-26 08:00	23-Jun-26 17:00	13-May-26 08:00 A	23-Jun-26 17:00 A	252.18	252.18	252.18	100%	100%	0




Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining W...
Milestone
summary

Baseline Schedule Rev.00

PLAYGROUNDS INITIATIVE - QASSIM, HAIL & TABUK - 25-Oct-2026

Activity ID	Activity Name	O.D	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Schedule % Complete	Performance % Complete	Variance - BL Project Duration
PG-H-CON-EX-TW-ST-20	PCC / Lean Concrete laying	27	20-May-26 08:00	24-Jun-26 17:00	20-May-26 08:00 A	24-Jun-26 17:00 A	168.12	168.12	168.12	100%	100%	0
PG-H-CON-EX-TW-ST-30	RCC Foundation(Completed)	13	10-Jun-26 08:00	24-Jun-26 17:00	10-Jun-26 08:00 A	24-Jun-26 17:00 A	766.58	766.58	766.58	100%	100%	0
PG-H-CON-EX-TW-ST-30_R	RCC Foundation(Remaining)	6	25-Jun-26 08:00	01-Jul-26 17:00	30-Jul-26 08:00 A	27-Aug-26 17:00 A	511.06	511.06	511.06	100%	100%	-19
PG-H-CON-EX-TW-ST-40	RCC Wall	7	02-Jul-26 08:00	09-Jul-26 17:00	14-Aug-26 08:00 A	15-Oct-26 17:00 A	2,757.60	2,757.60	2,757.60	100%	100%	-46
PG-H-CON-EX-TW-ST-50	RCC Slab	7	11-Jul-26 08:00	18-Jul-26 17:00	27-Aug-26 08:00 A	20-Oct-26 17:00 A	2,599.38	2,599.38	2,599.38	100%	100%	-39
PG-H-CON-EX-TW-ST-60	Finishing Work	7	17-Aug-26 08:00	24-Aug-26 17:00	24-Oct-26 08:00	31-Oct-26 17:00	252.18	0.00	252.18	100%	0%	0
PG-H-CON-EX-TW-ST-70	Backfilling	6	25-Aug-26 08:00	31-Aug-26 17:00	01-Nov-26 08:00	07-Nov-26 17:00	168.12	0.00	168.12	100%	0%	0
WATER STORAGE TANK		148	13-May-26 08:00	19-Sep-26 17:00	13-May-26 08:00 A	10-Nov-26 17:00	40,815.18	19,987.38	40,815.18	100%	48.97%	-44
PG-H-CON-EX-TW-IR-10	Excavation(Completed)	33	13-May-26 08:00	24-Jun-26 17:00	13-May-26 08:00 A	24-Jun-26 17:00 A	766.58	766.58	766.58	100%	100%	0
PG-H-CON-EX-TW-IR-10_R	Excavation(Remaining)	3	29-Aug-26 08:00	31-Aug-26 17:00	08-Jul-26 08:00 A	09-Jul-26 17:00 A	85.18	85.18	85.18	100%	100%	1
PG-H-CON-EX-TW-IR-20	RCC Foundation	6	01-Sep-26 08:00	07-Sep-26 17:00	23-Jul-26 08:00 A	27-Aug-26 17:00 A	4,136.40	4,136.40	4,136.40	100%	100%	-25
PG-H-CON-EX-TW-IR-30	Backfilling	5	08-Sep-26 08:00	13-Sep-26 17:00	14-Aug-26 08:00 A	27-Aug-26 17:00 A	1,114.02	1,114.02	1,114.02	100%	100%	-7
PG-H-CON-EX-TW-IR-40	GRP Water Tank Installation	5	14-Sep-26 08:00	19-Sep-26 17:00	17-Oct-26 08:00 A	10-Nov-26 17:00	34,713.00	13,885.20	34,713.00	100%	40%	-17
TOILET BUILDING WORKS		165	12-May-26 08:00	12-Oct-26 17:00	12-May-26 08:00 A	05-Nov-26 16:36	328,493.58	274,275.86	328,493.58	100%	83.5%	-21
CIVIL WORK		165	12-May-26 08:00	12-Oct-26 17:00	12-May-26 08:00 A	04-Nov-26 16:36	230,766.78	192,413.10	230,766.78	100%	83.38%	-20
STRUCTURAL WORK		59	12-May-26 08:00	22-Jul-26 17:00	12-May-26 08:00 A	23-Jul-26 17:00 A	37,980.00	37,980.00	37,980.00	100%	100%	-1
PG-H-CON-B-STR-10	Excavation up to bottom of footing	2	12-May-26 08:00	13-May-26 17:00	12-May-26 08:00 A	13-May-26 17:00 A	1,900.80	1,900.80	1,900.80	100%	100%	0
PG-H-CON-B-STR-20	Anti-termite treatment and Polyethene Sheet	2	12-May-26 08:00	13-May-26 17:00	12-May-26 08:00 A	13-May-26 17:00 A	3,294.00	3,294.00	3,294.00	100%	100%	0
PG-H-CON-B-STR-30	Backfilling with selected fill material (under footing)	1	13-May-26 08:00	13-May-26 17:00	13-May-26 08:00 A	13-May-26 17:00 A	1,900.80	1,900.80	1,900.80	100%	100%	0
PG-H-CON-B-STR-40	Raft Foundation Work	27	13-May-26 08:00	17-Jun-26 17:00	13-May-26 08:00 A	17-Jun-26 17:00 A	2,534.40	2,534.40	2,534.40	100%	100%	0
PG-H-CON-B-STR-50	Autoclaved aerated panel (walls)	4	13-Jul-26 08:00	16-Jul-26 17:00	11-Jul-26 08:00 A	12-Jul-26 17:00 A	11,340.00	11,340.00	11,340.00	100%	100%	2
PG-H-CON-B-STR-60	Autoclaved aerated panel (ceiling)	3	18-Jul-26 08:00	20-Jul-26 17:00	12-Jul-26 08:00 A	16-Jul-26 17:00 A	8,505.00	8,505.00	8,505.00	100%	100%	-2
PG-H-CON-B-STR-70	Autoclaved aerated panel (parapet)	2	21-Jul-26 08:00	22-Jul-26 17:00	12-Jul-26 08:00 A	23-Jul-26 17:00 A	8,505.00	8,505.00	8,505.00	100%	100%	-9
ARCHITECTURAL WORK		99	23-Jul-26 08:00	12-Oct-26 17:00	31-Jul-26 08:00 A	04-Nov-26 16:36	192,786.78	154,433.10	192,786.78	100%	80.11%	-13
GENERAL FINISHES		99	23-Jul-26 08:00	12-Oct-26 17:00	31-Jul-26 08:00 A	04-Nov-26 16:36	87,769.20	62,097.24	87,769.20	100%	70.75%	-13
PG-H-CON-B-AR-GF-10	Block Works	4	23-Jul-26 08:00	27-Jul-26 17:00	31-Jul-26 08:00 A	05-Aug-26 17:00 A	2,484.00	2,484.00	2,484.00	100%	100%	-1
PG-H-CON-B-AR-GF-20	Plaster	4	08-Aug-26 08:00	11-Aug-26 17:00	06-Aug-26 08:00 A	07-Aug-26 17:00 A	4,427.40	4,427.40	4,427.40	100%	100%	3
PG-H-CON-B-AR-GF-30	False Ceiling Installation & Finishing	8	20-Aug-26 08:00	29-Aug-26 17:00	20-Aug-26 08:00 A	15-Sep-26 09:36 A	873.60	873.60	873.60	100%	100%	-14
PG-H-CON-B-AR-GF-40	Wall Paint	3	09-Sep-26 08:00	12-Sep-26 17:00	20-Aug-26 08:00 A	29-Oct-26 15:00	2,958.00	2,366.40	2,958.00	100%	80%	-57
PG-H-CON-B-AR-GF-50	Epoxy Flooring	7	13-Sep-26 08:00	20-Sep-26 17:00	20-Aug-26 08:00 A	01-Nov-26 09:12	273.60	218.88	273.60	100%	80%	-54
PG-H-CON-B-AR-GF-60	Install Doors & Windows	5	21-Sep-26 08:00	27-Sep-26 17:00	27-Aug-26 08:00 A	02-Nov-26 09:12	13,273.80	10,619.04	13,273.80	100%	80%	-51
PG-H-CON-B-AR-GF-70	Facade Finishing Work	18	21-Sep-26 08:00	12-Oct-26 17:00	20-Aug-26 08:00 A	16-Sep-26 15:24 A	7,551.60	7,551.60	7,551.60	100%	100%	-6
PG-H-CON-B-AR-GF-80	Lockers and Furniture Installation	7	28-Sep-26 08:00	05-Oct-26 17:00	04-Oct-26 08:00 A	04-Nov-26 16:36	55,927.20	33,556.32	55,927.20	100%	60%	-21
WET AREA FINISHES		61	12-Aug-26 08:00	11-Oct-26 17:00	07-Aug-26 08:00 A	31-Oct-26 12:24	81,123.78	80,051.46	81,123.78	100%	98.68%	-21
PG-H-CON-B-AR-WF-10	False Ceiling Installation & Finishing	4	12-Aug-26 08:00	16-Aug-26 17:00	20-Aug-26 08:00 A	16-Sep-26 12:48 A	2,898.00	2,898.00	2,898.00	100%	100%	-20
PG-H-CON-B-AR-WF-20	Wall Tiles and Partition Work	3	13-Sep-26 08:00	15-Sep-26 17:00	07-Aug-26 08:00 A	14-Aug-26 17:00 A	21,283.20	21,283.20	21,283.20	100%	100%	-3
PG-H-CON-B-AR-WF-30	Waterproofing on Floor	2	16-Sep-26 08:00	17-Sep-26 17:00	14-Aug-26 08:00 A	16-Sep-26 12:48 A	5,784.00	5,784.00	5,784.00	100%	100%	-27
PG-H-CON-B-AR-WF-40	Floor Tiles Works	10	19-Sep-26 08:00	30-Sep-26 17:00	14-Aug-26 08:00 A	16-Sep-26 12:48 A	6,489.00	6,489.00	6,489.00	100%	100%	-19
PG-H-CON-B-AR-WF-50	Toilet accessories Installation Works	9	01-Oct-26 08:00	11-Oct-26 17:00	27-Aug-26 08:00 A	16-Sep-26 12:48 A	39,307.98	39,307.98	39,307.98	100%	100%	-9
PG-H-CON-B-AR-WF-60	Install Doors	4	01-Oct-26 08:00	05-Oct-26 17:00	27-Aug-26 08:00 A	31-Oct-26 12:24	5,361.60	4,289.28	5,361.60	100%	80%	-51
ROOF FINISHES		39	19-Sep-26 08:00	05-Oct-26 17:00	20-Aug-26 08:00 A	04-Nov-26 16:36	23,893.80	12,284.40	23,893.80	100%	51.41%	-51
PG-H-CON-B-AR-RF-10	Waterproofing on Floor	4	19-Sep-26 08:00	22-Sep-26 17:00	20-Aug-26 08:00 A	19-Oct-26 17:00 A	4,158.00	4,158.00	4,158.00	100%	100%	-47
PG-H-CON-B-AR-RF-20	Epoxy Flooring and Finishes	2	24-Sep-26 08:00	26-Sep-26 17:00	27-Aug-26 08:00 A	31-Oct-26 09:12	10,158.00	8,126.40	10,158.00	100%	80%	-52
PG-H-CON-B-AR-RF-30	Steel ladder and Steel roof scupper Installation	2	04-Oct-26 08:00	05-Oct-26 17:00	02-Nov-26 16:36	04-Nov-26 16:36	9,577.80	0.00	9,577.80	100%	0%	0
MEP WORK		75	28-Jul-26 08:00	05-Oct-26 17:00	22-Jul-26 08:00 A	05-Nov-26 16:36	97,726.80	81,862.76	97,726.80	100%	83.77%	-31
MECANICAL WORKS		75	28-Jul-26 08:00	06-Oct-26 17:00	22-Jul-26 08:00 A	05-Nov-26 16:36	79,479.48	66,055.00	79,479.48	100%	83.11%	-31
FIRE FIGHTING SYSTEM		1	06-Oct-26 08:00	06-Oct-26 17:00	04-Nov-26 16:36	05-Nov-26 16:36	136.26	0.00	136.26	100%	0%	0
PG-H-CON-B-GF-FF-10	Fire Extinguisher Installation	1	06-Oct-26 08:00	06-Oct-26 17:00	04-Nov-26 16:36	05-Nov-26 16:36	136.26	0.00	136.26	100%	0%	0
SEWER AND DRAINAGE SYSTEM		65	03-Aug-26 08:00	23-Aug-26 17:00	22-Jul-26 08:00 A	27-Oct-26 12:00	11,290.02	7,580.44	11,290.02	100%	67.14%	-65
PG-H-CON-B-GF-DR-10	Sewer and Drainge System Main Lines Installation	2	03-Aug-26 08:00	04-Aug-26 17:00	30-Jul-26 08:00 A	24-Oct-26 10:24	3,225.72	2,741.86	3,225.72	100%	85%	-70
PG-H-CON-B-GF-DR-20	Sewer and Drainge System Pipes and fittings Installation	2	18-Aug-26 08:00	19-Aug-26 17:00	22-Jul-26 08:00 A	05-Aug-26 17:00 A	4,838.58	4,838.58	4,838.58	100%	100%	-11
PG-H-CON-B-GF-DR-30	Sanitaryware Installation (Final Fix)	2	22-Aug-26 08:00	23-Aug-26 17:00	25-Oct-26 12:00	27-Oct-26 12:00	3,225.72	0.00	3,225.72	100%	0%	0
HVAC SYSTEM		31	28-Jul-26 08:00	15-Aug-26 17:00	13-Aug-26 08:00 A	24-Oct-26 16:12	12,127.20	9,821.76	12,127.20	100%	80.99%	-45
PG-H-CON-B-GF-AC-10	Duct Work and Exhaust Fan Installation	3	28-Jul-26 08:00	30-Jul-26 17:00	13-Aug-26 08:00 A	20-Aug-26 17:00 A	4,442.40	4,442.40	4,442.40	100%	100%	-4
PG-H-CON-B-GF-AC-20	Split AC, Grills & Diffuser Installation	3	12-Aug-26 08:00	15-Aug-26 17:00	26-Sep-26 08:00 A	24-Oct-26 16:12	7,684.80	5,379.36	7,684.80	100%	70%	-22
WATER SUPPLY SYSTEM		56	01-Aug-26 08:00	20-Aug-26 17:00	30-Jul-26 08:00 A	25-Oct-26 12:00	55,926.00	48,652.80	55,926.00	100%	86.99%	-56
PG-H-CON-B-GF-WS-10	Water Supply Main Lines Installation	2	01-Aug-26 08:00	02-Aug-26 17:00	30-Jul-26 08:00 A	31-Jul-26 17:00 A	5,702.40	5,702.40	5,702.40	100%	100%	1
PG-H-CON-B-GF-WS-20	Water Supply Pipes Installation (Cold and Hot Water)	2	16-Aug-26 08:00	17-Aug-26 17:00	30-Jul-26 08:00 A	06-Aug-26 17:00 A	13,857.60	13,857.60	13,857.60	100%	100%	-5
PG-H-CON-B-GF-WS-30	Water Supply Accesories and Booster pump Installation	3	18-Aug-26 08:00	20-Aug-26 17:00	27-Aug-26 08:00 A	25-Oct-26 12:00	36,366.00	29,092.80	36,366.00	100%	80%	-47
ELECTRICAL WORKS		40	05-Aug-26 08:00	08-Sep-26 17:00	12-Aug-26 08:00 A	29-Oct-26 09:12	18,247.32	15,807.76	18,247.32	100%	86.63%	-36
PG-H-CON-B-GF-EL-10	Pipes & Conduits Installation	2	05-Aug-26 08:00	06-Aug-26 17:00	12-Aug-26 08:00 A	14-Aug-26 17:00 A	1,983.60	1,983.60	1,983.60	100%	100%	0
PG-H-CON-B-GF-EL-20	Electrical Light Fixtures Installation	2	27-Aug-26 08:00	29-Aug-26 17:00	20-Aug-26 08:00 A	27-Oct-26 15:24	1,983.60	1,686.06	1,983.60	100%	85%	-56
PG-H-CON-B-GF-EL-30	Fire Alarm Devices Installation	3	30-Aug-26 08:00	01-Sep-26 17:00	20-Aug-26 08:00 A	28-Oct-26 10:00	1,983.60	1,686.06	1,983.60	100%	85%	-55
PG-H-CON-B-GF-EL-40	Telecom & CCTV Devices Installation	3	02-Sep-26 08:00	05-Sep-26 17:00	20-Aug-26 08:00 A	28-Oct-26 14:36	4,959.00	4,215.15	4,959.00	100%	85%	-56
PG-H-CON-B-GF-EL-50	Electrical & ELV Wiring Works	3	06-Sep-26 08:00	08-Sep-26 17:00	20-Aug-26 08:00 A	29-Oct-26 09:12	7,337.52	6,236.89	7,337.52	100%	85%	-56
PROJECT CLOSOUT		191	25-May-26 09:36	15-Dec-26 17:00	25-May-26 09:36 A	09-Jan-27 12:48	20,443.96	94,042.20	681,465.20	3%	13.8%	-21
PG-H-PCL-10	Testing, Commissioning for All Systems(Completed)	23	25-May-26 09:36	24-Jun-26 17:00	25-May-26 09:36 A	24-Jun-26 17:00 A	20,443.96	20,443.96	20,443.96	100%	100%	0
PG-H-PCL-10_R	Testing, Commissioning for All Systems(Remaining)	10	02-Nov-26 08:00	12-Nov-26 17:00	06-Aug-26 08:00 A	07-Dec-26 12:48	0.00	73,598.24	183,995.60	0%	40%	-95
PG-H-PCL-20	As-Built Drawings	18	14-Nov-26 08:00	03-Dec-26 17:00	07-Dec-26 12:48	28-Dec-26 12:48	0.00	0.00	68,146.52	0%	0%	0
PG-H-PCL-30	Snag list Submission	8	14-Nov-26 08:00	22-Nov-26 17:00	07-Dec-26 12:48	16-Dec-26 12:48	0.00	0.00	136,293.04	0%	0%	0
PG-H-PCL-40	Snag list Closeout	14	23-Nov-26 08:00	08-Dec-26 17:00	16-Dec-26 12:48	02-Jan-27 12:48	0.00	0.00	136,293.04	0%	0%	0
PG-H-PCL-50	Issuing Approvals	3	09-Dec-26 08:00	12-Dec-26 17:00	02-Jan-27 12:48	05-Jan-27 12:48	0.00	0.00	68,146.52	0%	0%	0
PG-H-PCL-60	Handing Over	3	13-Dec-26 08:00	15-Dec-26 17:00	05-Jan-27 12:48	09-Jan-27 12:48	0.00	0.00	68,146.52	0%	0%	0

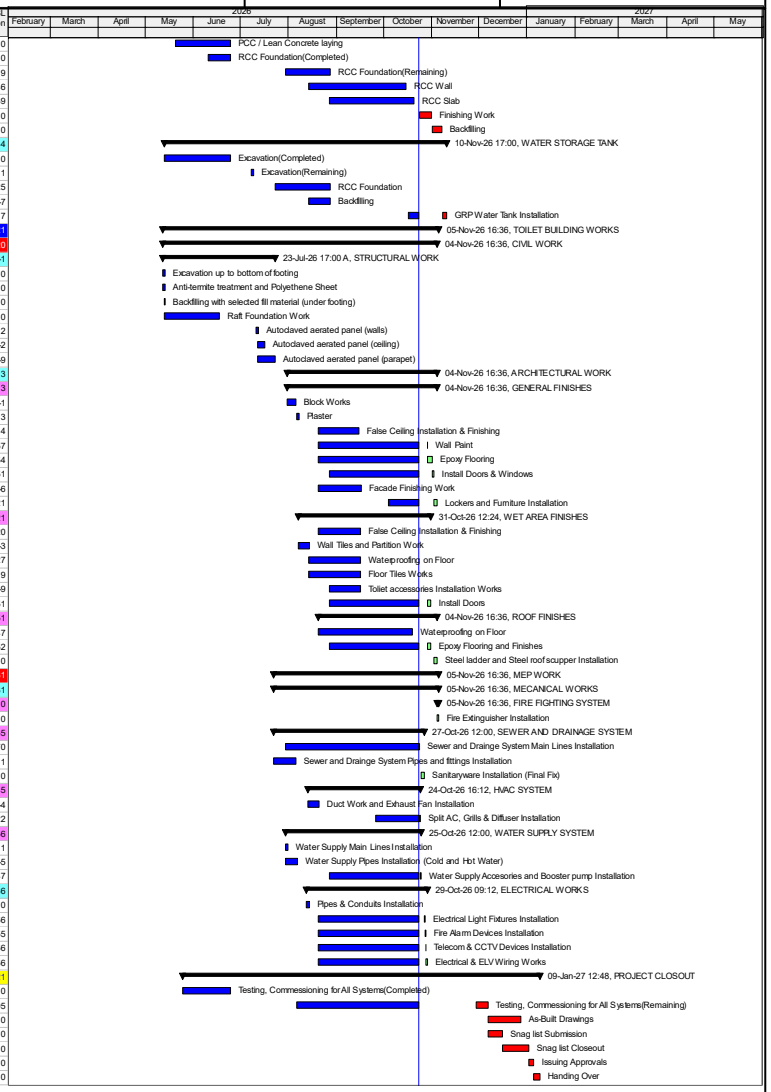

Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining W...
Milestone
summary

Baseline Schedule Rev.00

PLAYGROUNDS INITIATIVE - QASSIM, HAIL & TABUK - 25-Oct-2026

Activity ID	Activity Name	O.D	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Schedule % Complete	Performance % Complete	Variance - BL Project Duration
TABUK		299	17-Feb-26 08:00	16-Dec-26 17:00	17-Feb-26 08:00 A	11-Feb-27 17:00	8,880,320.41	6,802,182.48	11,357,801.00	78.19%	59.89%	-49
MOBILIZATION		44	17-Feb-26 08:00	15-Apr-26 10:00	17-Feb-26 08:00 A	14-Apr-26 17:00 A	0.00	0.00	0.00	0%	0%	0
TEMPORARY CAMP		43	17-Feb-26 08:00	14-Apr-26 10:00	17-Feb-26 08:00 A	13-Apr-26 17:00 A	0.00	0.00	0.00	0%	0%	0
PG-T-MOB-CAM-10	Temporary Underground Utilities works	43	17-Feb-26 08:00	14-Apr-26 10:00	17-Feb-26 08:00 A	13-Apr-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-T-MOB-CAM-20	Temporary Porta-Cabins	36	26-Feb-26 08:00	14-Apr-26 10:00	26-Feb-26 08:00 A	13-Apr-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-T-MOB-CAM-30	Temporary Toilets	36	26-Feb-26 08:00	14-Apr-26 10:00	26-Feb-26 08:00 A	13-Apr-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-T-MOB-CAM-40	Temporary Mosque	28	08-Mar-26 08:00	14-Apr-26 10:00	08-Mar-26 08:00 A	13-Apr-26 17:00 A	0.00	0.00	0.00	100%	100%	0
SITE OFFICES		44	17-Feb-26 08:00	15-Apr-26 10:00	17-Feb-26 08:00 A	14-Apr-26 17:00 A	0.00	0.00	0.00	0%	0%	0
PG-T-MOB-SO-10	Temporary Underground Utilities works	44	17-Feb-26 08:00	15-Apr-26 10:00	17-Feb-26 08:00 A	14-Apr-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-T-MOB-SO-20	Temporary Porta-Cabins	38	25-Feb-26 08:00	15-Apr-26 10:00	25-Feb-26 08:00 A	14-Apr-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-T-MOB-SO-30	Temporary Toilets	38	25-Feb-26 08:00	15-Apr-26 10:00	25-Feb-26 08:00 A	14-Apr-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-T-MOB-SO-40	Temporary Mosque	32	04-Mar-26 08:00	15-Apr-26 10:00	04-Mar-26 08:00 A	14-Apr-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-T-MOB-SO-50	Car Parking Area	25	12-Mar-26 08:00	15-Apr-26 10:00	12-Mar-26 08:00 A	14-Apr-26 17:00 A	0.00	0.00	0.00	100%	100%	0
GENERAL REQUIEREMENTS		44	17-Feb-26 08:00	15-Apr-26 10:00	17-Feb-26 08:00 A	14-Apr-26 17:00 A	0.00	0.00	0.00	0%	0%	0
PG-T-GEN-10	QA/QC Submission Plan	16	12-Mar-26 08:00	05-Apr-26 10:00	12-Mar-26 08:00 A	04-Apr-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-T-GEN-20	HSSE Submission Plan	35	17-Feb-26 08:00	05-Apr-26 10:00	17-Feb-26 08:00 A	04-Apr-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-T-GEN-30	Surveying report Submission Plan	44	17-Feb-26 08:00	15-Apr-26 10:00	17-Feb-26 08:00 A	14-Apr-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-T-GEN-40	Baseline Submission	6	28-Feb-26 08:00	07-Mar-26 10:00	28-Feb-26 08:00 A	05-Mar-26 17:00 A	0.00	0.00	0.00	100%	100%	0
ENGINEERING		171	17-Feb-26 08:00	12-Aug-26 17:00	17-Feb-26 08:00 A	17-Sep-26 11:12 A	340,734.03	340,734.03	340,734.03	100%	100%	-30
SHOP DRAWINGS SUBMITTALS		163	17-Feb-26 08:00	04-Aug-26 17:00	17-Feb-26 08:00 A	10-Sep-26 10:00 A	0.00	0.00	0.00	0%	0%	-31
STRUCTURAL DRAWINGS		135	17-Feb-26 08:00	18-Jul-26 17:00	17-Feb-26 08:00 A	03-Jul-26 17:00 A	0.00	0.00	0.00	0%	0%	13
PROJECT FENCE		63	17-Feb-26 08:00	07-May-26 10:00	17-Feb-26 08:00 A	06-May-26 17:00 A	0.00	0.00	0.00	0%	0%	0
PG-T-EN-STSD-SB-10	Excavation Drawings	63	17-Feb-26 08:00	07-May-26 10:00	17-Feb-26 08:00 A	06-May-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-T-EN-STSD-SB-20	Foundation Drawings	61	19-Feb-26 08:00	07-May-26 10:00	19-Feb-26 08:00 A	06-May-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PADEL PLAYGROUND FENCE		63	17-Feb-26 08:00	07-May-26 10:00	17-Feb-26 08:00 A	06-May-26 17:00 A	0.00	0.00	0.00	0%	0%	0
PG-T-EN-STSD-SB-30	Excavation Drawings	63	17-Feb-26 08:00	07-May-26 10:00	17-Feb-26 08:00 A	06-May-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-T-EN-STSD-SB-40	Foundation Drawings	61	19-Feb-26 08:00	07-May-26 10:00	19-Feb-26 08:00 A	06-May-26 17:00 A	0.00	0.00	0.00	100%	100%	0
AIR DOME		20	25-Jun-26 08:00	18-Jul-26 17:00	01-Jul-26 08:00 A	03-Jul-26 17:00 A	0.00	0.00	0.00	0%	0%	18
PG-T-EN-STSD-SB-50	Excavation Drawings	10	25-Jun-26 08:00	06-Jul-26 17:00	01-Jul-26 08:00 A	03-Jul-26 17:00 A	0.00	0.00	0.00	100%	100%	8
PG-T-EN-STSD-SB-60	Foundation Drawings	10	07-Jul-26 08:00	18-Jul-26 17:00	01-Jul-26 08:00 A	03-Jul-26 17:00 A	0.00	0.00	0.00	100%	100%	8
TOILET BUILDING		41	19-Feb-26 08:00	14-Apr-26 10:00	19-Feb-26 08:00 A	13-Apr-26 17:00 A	0.00	0.00	0.00	0%	0%	0
PG-T-EN-STSD-SB-70	Excavation Drawings	41	19-Feb-26 08:00	14-Apr-26 10:00	19-Feb-26 08:00 A	13-Apr-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-T-EN-STSD-SB-80	Foundation Drawings	39	23-Feb-26 08:00	14-Apr-26 10:00	23-Feb-26 08:00 A	13-Apr-26 17:00 A	0.00	0.00	0.00	100%	100%	0
WATER STORAGE TANK		39	23-Feb-26 08:00	14-Apr-26 10:00	23-Feb-26 08:00 A	13-Apr-26 17:00 A	0.00	0.00	0.00	0%	0%	0
PG-T-EN-STSD-SB-100	Foundation Drawings	37	25-Feb-26 08:00	14-Apr-26 10:00	25-Feb-26 08:00 A	13-Apr-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-T-EN-STSD-SB-90	Excavation Drawings	39	23-Feb-26 08:00	14-Apr-26 10:00	23-Feb-26 08:00 A	13-Apr-26 17:00 A	0.00	0.00	0.00	100%	100%	0
SEPTIC TANK		57	25-Feb-26 08:00	07-May-26 10:00	25-Feb-26 08:00 A	06-May-26 17:00 A	0.00	0.00	0.00	0%	0%	0
PG-T-EN-STSD-SB-110	Reinforcement Detail Drawings	57	25-Feb-26 08:00	07-May-26 10:00	25-Feb-26 08:00 A	06-May-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-T-EN-STSD-SB-120	Concrete Detail Drawings	54	01-Mar-26 08:00	07-May-26 10:00	01-Mar-26 08:00 A	06-May-26 17:00 A	0.00	0.00	0.00	100%	100%	0
ARCHITECTURAL DRAWINGS		150	23-Feb-26 08:00	04-Aug-26 17:00	23-Feb-26 08:00 A	10-Sep-26 10:00 A	0.00	0.00	0.00	0%	0%	-31
TOILET BUILDING		40	23-Feb-26 08:00	15-Apr-26 10:00	23-Feb-26 08:00 A	14-Apr-26 17:00 A	0.00	0.00	0.00	0%	0%	0
PG-T-EN-AR-SD-SB-10	Ground Floor Plan	40	23-Feb-26 08:00	15-Apr-26 10:00	23-Feb-26 08:00 A	14-Apr-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-T-EN-AR-SD-SB-100	Cladding Details	32	03-Mar-26 08:00	14-Apr-26 10:00	03-Mar-26 08:00 A	13-Apr-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-T-EN-AR-SD-SB-20	Roof Floor Plan	35	28-Feb-26 08:00	14-Apr-26 10:00	28-Feb-26 08:00 A	13-Apr-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-T-EN-AR-SD-SB-30	Elevations	33	03-Mar-26 08:00	15-Apr-26 10:00	03-Mar-26 08:00 A	14-Apr-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-T-EN-AR-SD-SB-40	Sections	31	05-Mar-26 08:00	15-Apr-26 10:00	05-Mar-26 08:00 A	14-Apr-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-T-EN-AR-SD-SB-50	Floor Finish Layout	36	28-Feb-26 08:00	14-Apr-26 13:00	28-Feb-26 08:00 A	14-Apr-26 12:00 A	0.00	0.00	0.00	100%	100%	0
PG-T-EN-AR-SD-SB-60	Reflected Ceiling Layout	36	28-Feb-26 08:00	15-Apr-26 10:00	28-Feb-26 08:00 A	14-Apr-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-T-EN-AR-SD-SB-70	Enlarged Toilets Layout	36	28-Feb-26 08:00	15-Apr-26 10:00	28-Feb-26 08:00 A	14-Apr-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-T-EN-AR-SD-SB-80	Doors & Windows Schedule	33	03-Mar-26 08:00	15-Apr-26 10:00	03-Mar-26 08:00 A	14-Apr-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-T-EN-AR-SD-SB-90	Aluminum Work	33	03-Mar-26 08:00	15-Apr-26 10:00	03-Mar-26 08:00 A	14-Apr-26 17:00 A	0.00	0.00	0.00	100%	100%	0
AIR DOME		15	19-Jul-26 08:00	04-Aug-26 17:00	05-Aug-26 08:00 A	10-Sep-26 10:00 A	0.00	0.00	0.00	0%	0%	-16
PG-T-EN-AR-SD-SB-110	Membrane & Insulation Details	15	19-Jul-26 08:00	04-Aug-26 17:00	05-Aug-26 08:00 A	10-Sep-26 10:00 A	0.00	0.00	0.00	100%	100%	-16
PG-T-EN-AR-SD-SB-120	Steel Cable System	15	19-Jul-26 08:00	04-Aug-26 17:00	05-Aug-26 08:00 A	10-Sep-26 10:00 A	0.00	0.00	0.00	100%	100%	-16
PG-T-EN-AR-SD-SB-130	Doors & Access Sytem Drawings	15	19-Jul-26 08:00	04-Aug-26 17:00	05-Aug-26 08:00 A	10-Sep-26 10:00 A	0.00	0.00	0.00	100%	100%	-16
LANDSCAPE DRAWINGS		40	23-Feb-26 08:00	15-Apr-26 10:00	23-Feb-26 08:00 A	14-Apr-26 17:00 A	0.00	0.00	0.00	0%	0%	0
PG-T-EN-LS-SD-SB-10	Hardscape Layout Plan	40	23-Feb-26 08:00	15-Apr-26 10:00	23-Feb-26 08:00 A	14-Apr-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-T-EN-LS-SD-SB-100	Padel Playground Layout	40	23-Feb-26 08:00	15-Apr-26 10:00	23-Feb-26 08:00 A	14-Apr-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-T-EN-LS-SD-SB-110	Basketball Playground Layout	40	23-Feb-26 08:00	15-Apr-26 10:00	23-Feb-26 08:00 A	14-Apr-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-T-EN-LS-SD-SB-120	Playground Details	40	23-Feb-26 08:00	15-Apr-26 10:00	23-Feb-26 08:00 A	14-Apr-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-T-EN-LS-SD-SB-130	Padel Fence Elevation & Details	40	23-Feb-26 08:00	15-Apr-26 10:00	23-Feb-26 08:00 A	14-Apr-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-T-EN-LS-SD-SB-20	Interlock Tile Details	40	23-Feb-26 08:00	15-Apr-26 10:00	23-Feb-26 08:00 A	14-Apr-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-T-EN-LS-SD-SB-30	Stamped Concrete Pattern & Section	40	23-Feb-26 08:00	15-Apr-26 10:00	23-Feb-26 08:00 A	14-Apr-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-T-EN-LS-SD-SB-40	Tartan Flooring Layout & Details	40	23-Feb-26 08:00	15-Apr-26 10:00	23-Feb-26 08:00 A	14-Apr-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-T-EN-LS-SD-SB-50	Bike Path Layout & Details	40	23-Feb-26 08:00	15-Apr-26 10:00	23-Feb-26 08:00 A	14-Apr-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-T-EN-LS-SD-SB-60	Walking Path layout & Details	40	23-Feb-26 08:00	15-Apr-26 10:00	23-Feb-26 08:00 A	14-Apr-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-T-EN-LS-SD-SB-70	Tree Planting Plan & Details	40	23-Feb-26 08:00	15-Apr-26 10:00	23-Feb-26 08:00 A	14-Apr-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-T-EN-LS-SD-SB-80	Traffic Sign Location & Details	40	23-Feb-26 08:00	15-Apr-26 10:00	23-Feb-26 08:00 A	14-Apr-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-T-EN-LS-SD-SB-90	Football Playground Layout	40	23-Feb-26 08:00	15-Apr-26 10:00	23-Feb-26 08:00 A	14-Apr-26 17:00 A	0.00	0.00	0.00	100%	100%	0
MECHANICAL DRAWINGS		140	28-Feb-26 08:00	12-Jul-26 17:00	28-Feb-26 08:00 A	13-Jul-26 17:00 A	0.00	0.00	0.00	0%	0%	-1
WATER SUPPLY SYSTEM		32	28-Feb-26 08:00	11-Apr-26 10:00	28-Feb-26 08:00 A	09-Apr-26 17:00 A	0.00	0.00	0.00	0%	0%	0
PG-T-EN-ME-SD-SB-10	Cold & Hot Water Piping Layout	28	04-Mar-26 08:00	11-Apr-26 10:00	04-Mar-26 08:00 A	09-Apr-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-T-EN-ME-SD-SB-20	Pump Room Layout	32	28-Feb-26 08:00	11-Apr-26 10:00	28-Feb-26 08:00 A	09-Apr-26 17:00 A	0.00	0.00	0.00	100%	100%	0




Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining W...
Milestone
summary

Baseline Schedule Rev.00

PLAYGROUNDS INITIATIVE - QASSIM, HAIL & TABUK - 25-Oct-2026

Activity ID	Activity Name	O.D	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Schedule % Complete	Performance % Complete	Variance - BL Project Duration
PG-T-EN-ME-SD-SB-30	Booster Pump Details	28	04-Mar-26 08:00	11-Apr-26 10:00	04-Mar-26 08:00 A	09-Apr-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-T-EN-ME-SD-SB-40	GRP Water Tank Details	24	09-Mar-26 08:00	11-Apr-26 10:00	09-Mar-26 08:00 A	09-Apr-26 17:00 A	0.00	0.00	0.00	100%	100%	0
SEWER AND DRAINAGE SYSTEM		28	04-Mar-26 08:00	11-Apr-26 10:00	04-Mar-26 08:00 A	09-Apr-26 17:00 A	0.00	0.00	0.00	0%	0%	0
PG-T-EN-ME-SD-SB-50	Drainage Layout	28	04-Mar-26 08:00	11-Apr-26 10:00	04-Mar-26 08:00 A	09-Apr-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-T-EN-ME-SD-SB-60	Floor Drains & Cleanouts Details	24	09-Mar-26 08:00	11-Apr-26 10:00	09-Mar-26 08:00 A	09-Apr-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-T-EN-ME-SD-SB-70	Inspection Chamber Details	21	12-Mar-26 08:00	11-Apr-26 10:00	12-Mar-26 08:00 A	09-Apr-26 17:00 A	0.00	0.00	0.00	100%	100%	0
IRRIGATION SYSTEM		47	09-Mar-26 08:00	07-May-26 10:00	09-Mar-26 08:00 A	06-May-26 17:00 A	0.00	0.00	0.00	0%	0%	0
PG-T-EN-ME-SD-SB-80	HDPE Pipe Routing	47	09-Mar-26 08:00	07-May-26 10:00	09-Mar-26 08:00 A	06-May-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-T-EN-ME-SD-SB-90	Irrigation Network Layout	44	12-Mar-26 08:00	07-May-26 10:00	12-Mar-26 08:00 A	06-May-26 17:00 A	0.00	0.00	0.00	100%	100%	0
AIR DOME		15	25-Jun-26 08:00	12-Jul-26 17:00	02-Jul-26 08:00 A	13-Jul-26 17:00 A	0.00	0.00	0.00	0%	0%	5
PG-T-EN-ME-SD-SB-100	Air Package and HVAC System Drawings	15	25-Jun-26 08:00	12-Jul-26 17:00	02-Jul-26 08:00 A	13-Jul-26 17:00 A	0.00	0.00	0.00	100%	100%	5
ELECTRICAL DRAWINGS		98	10-May-26 08:00	29-Jul-26 17:00	10-May-26 08:00 A	12-Jul-26 17:00 A	0.00	0.00	0.00	0%	0%	15
POWER AND LIGHTING SYSTEM		10	10-May-26 08:00	21-May-26 10:00	10-May-26 08:00 A	20-May-26 17:00 A	0.00	0.00	0.00	0%	0%	0
PG-T-EN-EL-SD-SB-10	Main Distribution Board (MDB) Layout	10	10-May-26 08:00	21-May-26 10:00	10-May-26 08:00 A	20-May-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-T-EN-EL-SD-SB-20	Pump Room Power Panel	10	10-May-26 08:00	21-May-26 10:00	10-May-26 08:00 A	20-May-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-T-EN-EL-SD-SB-30	Street Lighting Power Panel	10	10-May-26 08:00	21-May-26 10:00	10-May-26 08:00 A	20-May-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-T-EN-EL-SD-SB-40	Site Lighting Pole Layout	10	10-May-26 08:00	21-May-26 10:00	10-May-26 08:00 A	20-May-26 17:00 A	0.00	0.00	0.00	100%	100%	0
ELV SYSTEM		10	10-May-26 08:00	21-May-26 10:00	10-May-26 08:00 A	20-May-26 17:00 A	0.00	0.00	0.00	0%	0%	0
PG-T-EN-EL-SD-SB-50	Telecom & Data Layout	10	10-May-26 08:00	21-May-26 10:00	10-May-26 08:00 A	20-May-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-T-EN-EL-SD-SB-60	CCTV Camera Layout	10	10-May-26 08:00	21-May-26 10:00	10-May-26 08:00 A	20-May-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-T-EN-EL-SD-SB-70	Access Control Layout	10	10-May-26 08:00	21-May-26 10:00	10-May-26 08:00 A	20-May-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-T-EN-EL-SD-SB-80	AV System Layout	10	10-May-26 08:00	21-May-26 10:00	10-May-26 08:00 A	20-May-26 17:00 A	0.00	0.00	0.00	100%	100%	0
FIRE ALARM SYSTEM		10	10-May-26 08:00	21-May-26 10:00	10-May-26 08:00 A	20-May-26 17:00 A	0.00	0.00	0.00	0%	0%	0
PG-T-EN-EL-SD-SB-100	Detector & Manual Call Point Details	10	10-May-26 08:00	21-May-26 10:00	10-May-26 08:00 A	20-May-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-T-EN-EL-SD-SB-110	Control Panel Wiring Diagram	10	10-May-26 08:00	21-May-26 10:00	10-May-26 08:00 A	20-May-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-T-EN-EL-SD-SB-90	Fire Alarm Layout	10	10-May-26 08:00	21-May-26 10:00	10-May-26 08:00 A	20-May-26 17:00 A	0.00	0.00	0.00	100%	100%	0
AIR DOME		30	25-Jun-26 08:00	29-Jul-26 17:00	08-Jul-26 08:00 A	12-Jul-26 17:00 A	0.00	0.00	0.00	0%	0%	26
PG-T-EN-EL-SD-SB-120	Power & Lighting System Drawings	15	13-Jul-26 08:00	29-Jul-26 17:00	08-Jul-26 08:00 A	12-Jul-26 17:00 A	0.00	0.00	0.00	100%	100%	11
PG-T-EN-EL-SD-SB-130	Generators Details	15	25-Jun-26 08:00	12-Jul-26 17:00	08-Jul-26 08:00 A	12-Jul-26 17:00 A	0.00	0.00	0.00	100%	100%	11
PG-T-EN-EL-SD-SB-140	Smart Dome System Drawings	15	13-Jul-26 08:00	29-Jul-26 17:00	08-Jul-26 08:00 A	12-Jul-26 17:00 A	0.00	0.00	0.00	100%	100%	11
SHOP DRAWINGS APPROVALS		169	19-Feb-26 08:00	12-Aug-26 17:00	19-Feb-26 08:00 A	02-Sep-26 15:00 A	0.00	0.00	0.00	0%	0%	-18
STRUCTURAL DRAWINGS		138	19-Feb-26 08:00	23-Jul-26 17:00	19-Feb-26 08:00 A	11-Jul-26 08:00 A	0.00	0.00	0.00	0%	0%	12
PROJECT FENCE		61	19-Feb-26 08:00	07-May-26 10:00	19-Feb-26 08:00 A	06-May-26 17:00 A	0.00	0.00	0.00	0%	0%	0
PG-T-EN-STSD-AP-10	Excavation Drawings	61	19-Feb-26 08:00	07-May-26 10:00	19-Feb-26 08:00 A	06-May-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-T-EN-STSD-AP-20	Foundation Drawings	58	24-Feb-26 08:00	07-May-26 10:00	24-Feb-26 08:00 A	06-May-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PADEL PLAYGROUND FENCE		61	19-Feb-26 08:00	07-May-26 10:00	19-Feb-26 08:00 A	06-May-26 17:00 A	0.00	0.00	0.00	0%	0%	0
PG-T-EN-STSD-AP-30	Excavation Drawings	61	19-Feb-26 08:00	07-May-26 10:00	19-Feb-26 08:00 A	06-May-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-T-EN-STSD-AP-40	Foundation Drawings	58	24-Feb-26 08:00	07-May-26 10:00	24-Feb-26 08:00 A	06-May-26 17:00 A	0.00	0.00	0.00	100%	100%	0
AIR DOME		15	07-Jul-26 08:00	23-Jul-26 17:00	05-Jul-26 08:00 A	11-Jul-26 08:00 A	0.00	0.00	0.00	0%	0%	10
PG-T-EN-STSD-AP-50	Excavation Drawings	5	07-Jul-26 08:00	12-Jul-26 17:00	08-Jul-26 08:00 A	11-Jul-26 08:00 A	0.00	0.00	0.00	100%	100%	3
PG-T-EN-STSD-AP-60	Foundation Drawings	5	19-Jul-26 08:00	23-Jul-26 17:00	05-Jul-26 08:00 A	06-Jul-26 17:00 A	0.00	0.00	0.00	100%	100%	3
TOILET BUILDING		42	23-Feb-26 08:00	18-Apr-26 10:00	23-Feb-26 08:00 A	16-Apr-26 17:00 A	0.00	0.00	0.00	0%	0%	0
PG-T-EN-STSD-AP-70	Excavation Drawings	42	23-Feb-26 08:00	18-Apr-26 10:00	23-Feb-26 08:00 A	16-Apr-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-T-EN-STSD-AP-80	Foundation Drawings	39	26-Feb-26 08:00	18-Apr-26 10:00	26-Feb-26 08:00 A	16-Apr-26 17:00 A	0.00	0.00	0.00	100%	100%	0
WATER STORAGE TANK		40	25-Feb-26 08:00	18-Apr-26 10:00	25-Feb-26 08:00 A	16-Apr-26 17:00 A	0.00	0.00	0.00	0%	0%	0
PG-T-EN-STSD-AP-100	Foundation Drawings	37	01-Mar-26 08:00	18-Apr-26 10:00	01-Mar-26 08:00 A	16-Apr-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-T-EN-STSD-AP-90	Excavation Drawings	40	25-Feb-26 08:00	18-Apr-26 10:00	25-Feb-26 08:00 A	16-Apr-26 17:00 A	0.00	0.00	0.00	100%	100%	0
SEPTIC TANK		54	01-Mar-26 08:00	07-May-26 10:00	01-Mar-26 08:00 A	06-May-26 17:00 A	0.00	0.00	0.00	0%	0%	0
PG-T-EN-STSD-AP-110	Reinforcement Detail Drawings	54	01-Mar-26 08:00	07-May-26 10:00	01-Mar-26 08:00 A	06-May-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-T-EN-STSD-AP-120	Concrete Detail Drawings	51	04-Mar-26 08:00	07-May-26 10:00	04-Mar-26 08:00 A	06-May-26 17:00 A	0.00	0.00	0.00	100%	100%	0
ARCHITECTURAL DRAWINGS		153	28-Feb-26 08:00	12-Aug-26 17:00	28-Feb-26 08:00 A	02-Sep-26 15:00 A	0.00	0.00	0.00	0%	0%	-18
TOILET BUILDING		38	28-Feb-26 08:00	18-Apr-26 10:00	28-Feb-26 08:00 A	16-Apr-26 17:00 A	0.00	0.00	0.00	0%	0%	0
PG-T-EN-AR-SD-AP-10	Ground Floor Plan	38	28-Feb-26 08:00	18-Apr-26 10:00	28-Feb-26 08:00 A	16-Apr-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-T-EN-AR-SD-AP-100	Cladding Details	31	08-Mar-26 08:00	18-Apr-26 10:00	08-Mar-26 08:00 A	16-Apr-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-T-EN-AR-SD-AP-20	Roof Floor Plan	35	03-Mar-26 08:00	18-Apr-26 10:00	03-Mar-26 08:00 A	16-Apr-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-T-EN-AR-SD-AP-30	Elevations	32	07-Mar-26 08:00	18-Apr-26 10:00	07-Mar-26 08:00 A	16-Apr-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-T-EN-AR-SD-AP-40	Sections	29	10-Mar-26 08:00	18-Apr-26 10:00	10-Mar-26 08:00 A	16-Apr-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-T-EN-AR-SD-AP-50	Floor Finish Layout	33	05-Mar-26 08:00	18-Apr-26 10:00	05-Mar-26 08:00 A	16-Apr-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-T-EN-AR-SD-AP-60	Reflected Ceiling Layout	33	05-Mar-26 08:00	18-Apr-26 10:00	05-Mar-26 08:00 A	16-Apr-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-T-EN-AR-SD-AP-70	Enlarged Toilets Layout	33	05-Mar-26 08:00	18-Apr-26 10:00	05-Mar-26 08:00 A	16-Apr-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-T-EN-AR-SD-AP-80	Doors & Windows Schedule	32	07-Mar-26 08:00	18-Apr-26 10:00	07-Mar-26 08:00 A	16-Apr-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-T-EN-AR-SD-AP-90	Aluminum Work	31	08-Mar-26 08:00	18-Apr-26 10:00	08-Mar-26 08:00 A	16-Apr-26 17:00 A	0.00	0.00	0.00	100%	100%	0
AIR DOME		7	05-Aug-26 08:00	12-Aug-26 17:00	06-Aug-26 08:00 A	02-Sep-26 15:00 A	0.00	0.00	0.00	0%	0%	-17
PG-T-EN-AR-SD-AP-110	Membrane & Insulation Details	7	05-Aug-26 08:00	12-Aug-26 17:00	06-Aug-26 08:00 A	02-Sep-26 15:00 A	0.00	0.00	0.00	100%	100%	-17
PG-T-EN-AR-SD-AP-120	Steel Cable System	7	05-Aug-26 08:00	12-Aug-26 17:00	06-Aug-26 08:00 A	02-Sep-26 15:00 A	0.00	0.00	0.00	100%	100%	-17
PG-T-EN-AR-SD-AP-130	Doors & Access Sytem Drawings	7	05-Aug-26 08:00	12-Aug-26 17:00	06-Aug-26 08:00 A	02-Sep-26 15:00 A	0.00	0.00	0.00	100%	100%	-17
LANDSCAPE DRAWINGS		39	26-Feb-26 08:00	18-Apr-26 10:00	26-Feb-26 08:00 A	16-Apr-26 17:00 A	0.00	0.00	0.00	0%	0%	0
PG-T-EN-LS-SD-AP-10	Hardscape Layout Plan	38	28-Feb-26 08:00	18-Apr-26 10:00	28-Feb-26 08:00 A	16-Apr-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-T-EN-LS-SD-AP-100	Padel Playground Layout	38	28-Feb-26 08:00	18-Apr-26 10:00	28-Feb-26 08:00 A	16-Apr-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-T-EN-LS-SD-AP-110	Basketball Playground Layout	38	28-Feb-26 08:00	18-Apr-26 10:00	28-Feb-26 08:00 A	16-Apr-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-T-EN-LS-SD-AP-120	Playground Details	38	28-Feb-26 08:00	18-Apr-26 10:00	28-Feb-26 08:00 A	16-Apr-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-T-EN-LS-SD-AP-130	Padel Fence Elevation & Details	39	26-Feb-26 08:00	18-Apr-26 10:00	26-Feb-26 08:00 A	16-Apr-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-T-EN-LS-SD-AP-20	Interlock Tile Details	30	09-Mar-26 08:00	18-Apr-26 10:00	09-Mar-26 08:00 A	16-Apr-26 17:00 A	0.00	0.00	0.00	100%	100%	0

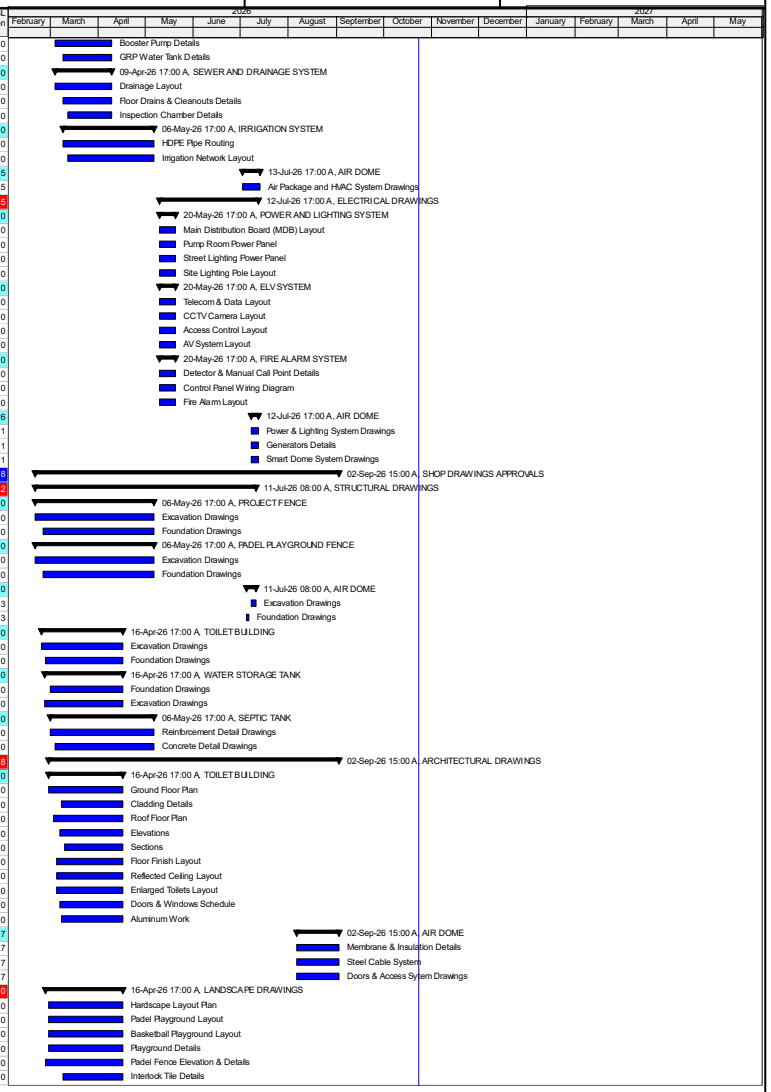


Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining W...
Milestone
summary

Baseline Schedule Rev.00

PLAYGROUNDS INITIATIVE - QASSIM, HAIL & TABUK - 25-Oct-2026

Activity ID	Activity Name	O.D	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Schedule % Complete	Performance % Complete	Variance - BL Project Duration
PG-T-EN-LS-SD-AP-30	Stamped Concrete Pattern & Section	24	16-Mar-26 08:00	18-Apr-26 10:00	16-Mar-26 08:00 A	16-Apr-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-T-EN-LS-SD-AP-40	Tartan Flooring Layout & Details	38	28-Feb-26 08:00	18-Apr-26 10:00	28-Feb-26 08:00 A	16-Apr-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-T-EN-LS-SD-AP-50	Bike Path Layout & Details	39	26-Feb-26 08:00	18-Apr-26 10:00	26-Feb-26 08:00 A	16-Apr-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-T-EN-LS-SD-AP-60	Walking Path layout & Details	39	26-Feb-26 08:00	18-Apr-26 10:00	26-Feb-26 08:00 A	16-Apr-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-T-EN-LS-SD-AP-70	Tee Planting Plan & Details	38	28-Feb-26 08:00	18-Apr-26 10:00	28-Feb-26 08:00 A	16-Apr-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-T-EN-LS-SD-AP-80	Traffic Sign Location & Details	39	26-Feb-26 08:00	18-Apr-26 10:00	26-Feb-26 08:00 A	16-Apr-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-T-EN-LS-SD-AP-90	Football Playground Layout	38	28-Feb-26 08:00	18-Apr-26 10:00	28-Feb-26 08:00 A	16-Apr-26 17:00 A	0.00	0.00	0.00	100%	100%	0
MECHANICAL DRAWINGS		142	09-Mar-26 08:00	23-Jul-26 17:00	09-Mar-26 08:00 A	18-Jul-26 17:00 A	0.00	0.00	0.00	0%	0%	5
WATER SUPPLY SYSTEM		27	09-Mar-26 08:00	14-Apr-26 10:00	09-Mar-26 08:00 A	13-Apr-26 17:00 A	0.00	0.00	0.00	0%	0%	0
PG-T-EN-ME-SD-AP-10	Cold & Hot Water Piping Layout	27	09-Mar-26 08:00	14-Apr-26 10:00	09-Mar-26 08:00 A	13-Apr-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-T-EN-ME-SD-AP-20	Pump Room Layout	21	16-Mar-26 08:00	14-Apr-26 10:00	16-Mar-26 08:00 A	13-Apr-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-T-EN-ME-SD-AP-30	Booster Pump Details	26	10-Mar-26 08:00	14-Apr-26 10:00	10-Mar-26 08:00 A	13-Apr-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-T-EN-ME-SD-AP40	GRP Water Tank Details	23	14-Mar-26 08:00	14-Apr-26 10:00	14-Mar-26 08:00 A	13-Apr-26 17:00 A	0.00	0.00	0.00	100%	100%	0
SEWER AND DRAINAGE SYSTEM		27	09-Mar-26 08:00	14-Apr-26 10:00	09-Mar-26 08:00 A	13-Apr-26 17:00 A	0.00	0.00	0.00	0%	0%	0
PG-T-EN-ME-SD-AP-50	Drainage Layout	27	09-Mar-26 08:00	14-Apr-26 10:00	09-Mar-26 08:00 A	13-Apr-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-T-EN-ME-SD-AP-60	Floor Drains & Cleanouts Details	21	16-Mar-26 08:00	14-Apr-26 10:00	16-Mar-26 08:00 A	13-Apr-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-T-EN-ME-SD-AP-70	Inspection Chamber Details	21	16-Mar-26 08:00	14-Apr-26 10:00	16-Mar-26 08:00 A	13-Apr-26 17:00 A	0.00	0.00	0.00	100%	100%	0
IRRIGATION SYSTEM		44	12-Mar-26 08:00	07-May-26 10:00	12-Mar-26 08:00 A	06-May-26 17:00 A	0.00	0.00	0.00	0%	0%	0
PG-T-EN-ME-SD-AP-80	HDPE Pipe Routing	44	12-Mar-26 08:00	07-May-26 10:00	12-Mar-26 08:00 A	06-May-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-T-EN-ME-SD-AP-90	Irrigation Network Layout	40	17-Mar-26 08:00	07-May-26 10:00	17-Mar-26 08:00 A	06-May-26 17:00 A	0.00	0.00	0.00	100%	100%	0
AIR DOME		10	13-Jul-26 08:00	23-Jul-26 17:00	13-Jul-26 08:00 A	18-Jul-26 17:00 A	0.00	0.00	0.00	0%	0%	5
PG-T-EN-ME-SD-AP-100	Air Package and HVAC System Drawings	10	13-Jul-26 08:00	23-Jul-26 17:00	13-Jul-26 08:00 A	18-Jul-26 17:00 A	0.00	0.00	0.00	100%	100%	5
ELECTRICAL DRAWINGS		105	11-May-26 08:00	08-Aug-26 17:00	11-May-26 08:00 A	19-Jul-26 17:00 A	0.00	0.00	0.00	0%	0%	17
POWER AND LIGHTING SYSTEM		28	11-May-26 08:00	17-Jun-26 10:00	11-May-26 08:00 A	16-Jun-26 17:00 A	0.00	0.00	0.00	0%	0%	0
PG-T-EN-EL-SD-AP-10	Main Distribution Board (MDB) Layout	28	11-May-26 08:00	17-Jun-26 10:00	11-May-26 08:00 A	16-Jun-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-T-EN-EL-SD-AP-20	Pump Room Power Panel	28	11-May-26 08:00	17-Jun-26 10:00	11-May-26 08:00 A	16-Jun-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-T-EN-EL-SD-AP-30	Street Lighting Power Panel	28	11-May-26 08:00	17-Jun-26 10:00	11-May-26 08:00 A	16-Jun-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-T-EN-EL-SD-AP-40	Site Lighting Pole Layout	28	11-May-26 08:00	17-Jun-26 10:00	11-May-26 08:00 A	16-Jun-26 17:00 A	0.00	0.00	0.00	100%	100%	0
ELV SYSTEM		28	11-May-26 08:00	17-Jun-26 10:00	11-May-26 08:00 A	16-Jun-26 17:00 A	0.00	0.00	0.00	0%	0%	0
PG-T-EN-EL-SD-AP-50	Telecom & Data Layout	28	11-May-26 08:00	17-Jun-26 10:00	11-May-26 08:00 A	16-Jun-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-T-EN-EL-SD-AP-60	CCTV Camera Layout	28	11-May-26 08:00	17-Jun-26 10:00	11-May-26 08:00 A	16-Jun-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-T-EN-EL-SD-AP-70	Access Control Layout	28	11-May-26 08:00	17-Jun-26 10:00	11-May-26 08:00 A	16-Jun-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-T-EN-EL-SD-AP-80	AV System Layout	28	11-May-26 08:00	17-Jun-26 10:00	11-May-26 08:00 A	16-Jun-26 17:00 A	0.00	0.00	0.00	100%	100%	0
FIRE ALARM SYSTEM		28	11-May-26 08:00	17-Jun-26 10:00	11-May-26 08:00 A	16-Jun-26 17:00 A	0.00	0.00	0.00	0%	0%	0
PG-T-EN-EL-SD-AP-100	Detector & Manual Call Point Details	28	11-May-26 08:00	17-Jun-26 10:00	11-May-26 08:00 A	16-Jun-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-T-EN-EL-SD-AP-110	Control Panel Wiring Diagram	28	11-May-26 08:00	17-Jun-26 10:00	11-May-26 08:00 A	16-Jun-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-T-EN-EL-SD-AP-90	Fire Alarm Layout	28	11-May-26 08:00	17-Jun-26 10:00	11-May-26 08:00 A	16-Jun-26 17:00 A	0.00	0.00	0.00	100%	100%	0
AIR DOME		23	13-Jul-26 08:00	08-Aug-26 17:00	13-Jul-26 08:00 A	19-Jul-26 17:00 A	0.00	0.00	0.00	0%	0%	17
PG-T-EN-EL-SD-AP-120	Power & Lighting System Drawings	8	30-Jul-26 08:00	08-Aug-26 17:00	13-Jul-26 08:00 A	19-Jul-26 17:00 A	0.00	0.00	0.00	100%	100%	2
PG-T-EN-EL-SD-AP-130	Generators Details	8	13-Jul-26 08:00	21-Jul-26 17:00	13-Jul-26 08:00 A	19-Jul-26 17:00 A	0.00	0.00	0.00	100%	100%	2
PG-T-EN-EL-SD-AP-140	Smart Dome System Drawings	8	30-Jul-26 08:00	08-Aug-26 17:00	13-Jul-26 08:00 A	19-Jul-26 17:00 A	0.00	0.00	0.00	100%	100%	2
MATERIAL SUBMITTALS		166	17-Feb-26 08:00	11-Jul-26 17:00	17-Feb-26 08:00 A	15-Sep-26 12:00 A	0.00	0.00	0.00	0%	0%	-57
LONG LEAD ITEMS		166	17-Feb-26 08:00	11-Jul-26 17:00	17-Feb-26 08:00 A	15-Sep-26 12:00 A	0.00	0.00	0.00	0%	0%	-57
EXTERNAL / LANDSCAPE WORK		57	25-Feb-26 08:00	07-May-26 10:00	25-Feb-26 08:00 A	06-May-26 17:00 A	0.00	0.00	0.00	0%	0%	0
PG-T-PR-LL-LS-MS-10	Bike and Walk Path Materials	50	05-Mar-26 08:00	07-May-26 10:00	05-Mar-26 08:00 A	06-May-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-T-PR-LL-LS-MS-20	Benches, Seats (Rectangular & Circular)	57	25-Feb-26 08:00	07-May-26 10:00	25-Feb-26 08:00 A	06-May-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-T-PR-LL-LS-MS-30	Fence, gates and accessories	50	05-Mar-26 08:00	07-May-26 10:00	05-Mar-26 08:00 A	06-May-26 17:00 A	0.00	0.00	0.00	100%	100%	0
SPORTS & RECREATIONAL FACILITIES WORK		124	17-Feb-26 08:00	05-Jul-26 17:00	17-Feb-26 08:00 A	02-Sep-26 17:00 A	0.00	0.00	0.00	0%	0%	-51
PG-T-PR-LL-SPMS-10	Football Playground Materials (Flooring, goal post, nets, paints, etc)	49	07-Mar-26 08:00	07-May-26 10:00	07-Mar-26 08:00 A	06-May-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-T-PR-LL-SPMS-20	Basketball Playground Materials (Flooring, basketball poll, nets, paints,	49	07-Mar-26 08:00	07-May-26 10:00	07-Mar-26 08:00 A	06-May-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-T-PR-LL-SPMS-30	Padel Playground Materials (Flooring, fence, tempered glass, etc)	49	07-Mar-26 08:00	07-May-26 10:00	07-Mar-26 08:00 A	06-May-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-T-PR-LL-SPMS-40	Tartan Floor	49	07-Mar-26 08:00	07-May-26 10:00	07-Mar-26 08:00 A	06-May-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-T-PR-LL-SPMS-50	Air Dome Materials(Completed)	101	17-Feb-26 08:00	25-Jun-26 10:00	17-Feb-26 08:00 A	24-Jun-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-T-PR-LL-SPMS-50_R	Air Dome Materials(Remaining)	9	25-Jun-26 08:00	05-Jul-26 17:00	07-Jul-26 08:00 A	02-Sep-26 17:00 A	0.00	0.00	0.00	100%	100%	-41
CONCRETE WORK		41	07-Mar-26 08:00	28-Apr-26 10:00	07-Mar-26 08:00 A	27-Apr-26 17:00 A	0.00	0.00	0.00	0%	0%	0
PG-T-PR-LL-CO-MS-10	Autoclaved Aerated Panel	41	07-Mar-26 08:00	28-Apr-26 10:00	07-Mar-26 08:00 A	27-Apr-26 17:00 A	0.00	0.00	0.00	100%	100%	0
METAL WORK		45	11-Mar-26 08:00	07-May-26 10:00	11-Mar-26 08:00 A	06-May-26 17:00 A	0.00	0.00	0.00	0%	0%	0
PG-T-PR-LL-MT-MS-10	Metal Doors	45	11-Mar-26 08:00	07-May-26 10:00	11-Mar-26 08:00 A	06-May-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-T-PR-LL-MT-MS-20	Curtain Wall	45	11-Mar-26 08:00	07-May-26 10:00	11-Mar-26 08:00 A	06-May-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PLUMBING WORK		46	10-Mar-26 08:00	07-May-26 10:00	10-Mar-26 08:00 A	06-May-26 17:00 A	0.00	0.00	0.00	0%	0%	0
PG-T-PR-LL-PB-MS-10	Booster Pump	46	10-Mar-26 08:00	07-May-26 10:00	10-Mar-26 08:00 A	06-May-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-T-PR-LL-PB-MS-20	GRP Sectional Panel Water Tanks (4x3x3m)	42	15-Mar-26 08:00	07-May-26 10:00	15-Mar-26 08:00 A	06-May-26 17:00 A	0.00	0.00	0.00	100%	100%	0
IRRIGATION WORK		50	05-Mar-26 08:00	07-May-26 10:00	05-Mar-26 08:00 A	06-May-26 17:00 A	0.00	0.00	0.00	0%	0%	0
PG-T-PR-LL-IR-MS-10	HDPE Pipes	50	05-Mar-26 08:00	07-May-26 10:00	05-Mar-26 08:00 A	06-May-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-T-PR-LL-IR-MS-20	Irrigation Control System	50	05-Mar-26 08:00	07-May-26 10:00	05-Mar-26 08:00 A	06-May-26 17:00 A	0.00	0.00	0.00	100%	100%	0
ELECTRICAL WORK		100	11-May-26 08:00	11-Jul-26 17:00	11-May-26 08:00 A	15-Sep-26 12:00 A	0.00	0.00	0.00	0%	0%	-57
PG-T-PR-LL-EL-MS-10	Main Distribution Board(Completed)	35	11-May-26 08:00	25-Jun-26 10:00	11-May-26 08:00 A	24-Jun-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-T-PR-LL-EL-MS-10_R	Main Distribution Board(Remaining)	10	25-Jun-26 08:00	06-Jul-26 17:00	16-Jul-26 08:00 A	05-Aug-26 17:00 A	0.00	0.00	0.00	100%	100%	-8
PG-T-PR-LL-EL-MS-20	Power Panels (Pump, Street Light)(Completed)	35	11-May-26 08:00	25-Jun-26 10:00	11-May-26 08:00 A	24-Jun-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-T-PR-LL-EL-MS-20_R	Power Panels (Pump, Street Light)(Remaining)	10	25-Jun-26 08:00	06-Jul-26 17:00	16-Jul-26 08:00 A	05-Aug-26 17:00 A	0.00	0.00	0.00	100%	100%	-8
PG-T-PR-LL-EL-MS-30	Site Lighting Poles(Completed)	35	11-May-26 08:00	25-Jun-26 10:00	11-May-26 08:00 A	24-Jun-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-T-PR-LL-EL-MS-30_R	Site Lighting Poles(Remaining)	10	25-Jun-26 08:00	06-Jul-26 17:00	16-Jul-26 08:00 A	05-Aug-26 17:00 A	0.00	0.00	0.00	100%	100%	-8
PG-T-PR-LL-EL-MS-40	Lighting Fixtures(Completed)	35	11-May-26 08:00	25-Jun-26 10:00	11-May-26 08:00 A	24-Jun-26 17:00 A	0.00	0.00	0.00	100%	100%	0

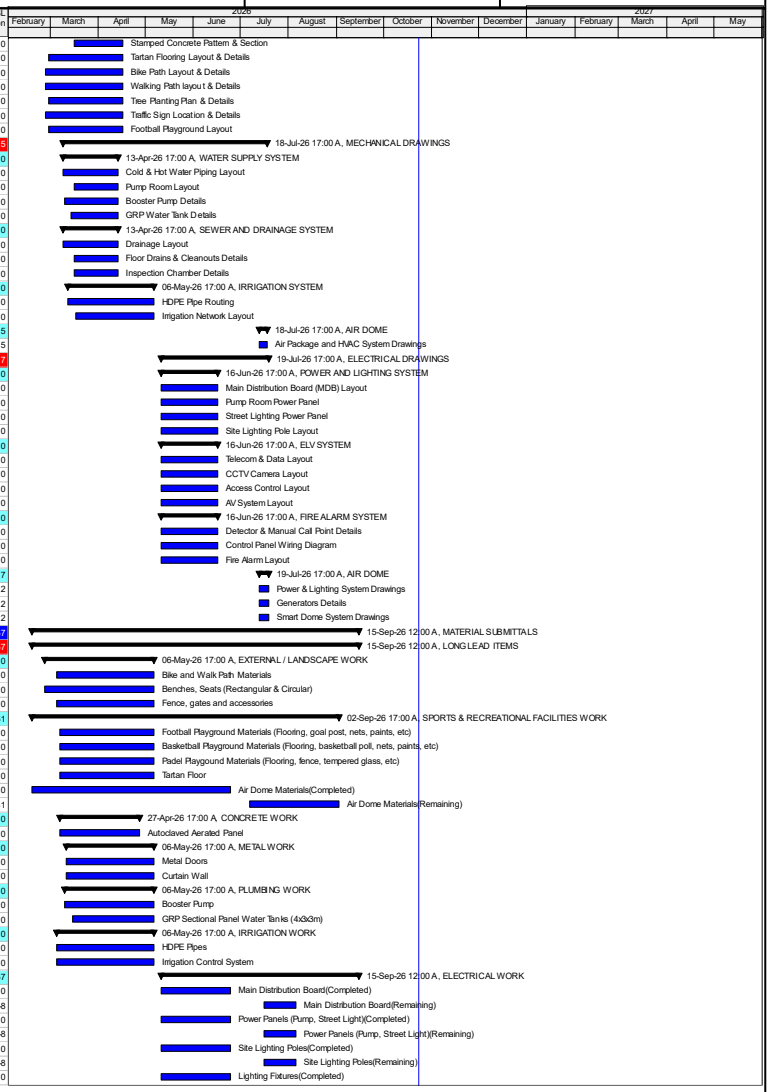


Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining W...
Milestone
summary

Baseline Schedule Rev.00

PLAYGROUNDS INITIATIVE - QASSIM, HAIL & TABUK - 25-Oct-2026

Activity ID	Activity Name	O.D	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Schedule % Complete	Performance % Complete	Variance - BL Project Duration
PG-T-PR-LL-EL-MS-40_R	Lighting Fixtures(Remaining)	10	25-Jun-26 08:00	06-Jul-26 17:00	16-Jul-26 08:00 A	22-Jul-26 17:00 A	0.00	0.00	0.00	100%	100%	4
PG-T-PR-LL-EL-MS-50	Grounding System Materials (Earth pit rod, LPS, etc)(Completed)	35	11-May-26 08:00	25-Jun-26 10:00	11-May-26 08:00 A	24-Jun-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-T-PR-LL-EL-MS-50_R	Grounding System Materials (Earth pit rod, LPS, etc)(Remaining)	5	06-Jul-26 08:00	11-Jul-26 17:00	16-Jul-26 08:00 A	20-Jul-26 17:00 A	0.00	0.00	0.00	100%	100%	1
PG-T-PR-LL-EL-MS-60	Telecommunications & Data System Materials (Telephone outlet, CCTV,	35	11-May-26 08:00	25-Jun-26 10:00	11-May-26 08:00 A	24-Jun-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-T-PR-LL-EL-MS-60_R	Telecommunications & Data System Materials (Telephone outlet, CCTV,	10	25-Jun-26 08:00	06-Jul-26 17:00	16-Jul-26 08:00 A	15-Sep-26 12:00 A	0.00	0.00	0.00	100%	100%	-43
PG-T-PR-LL-EL-MS-70	Security and Access Control System Materials(Completed)	35	11-May-26 08:00	25-Jun-26 10:00	11-May-26 08:00 A	24-Jun-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-T-PR-LL-EL-MS-70_R	Security and Access Control System Materials(Remaining)	10	25-Jun-26 08:00	06-Jul-26 17:00	16-Jul-26 08:00 A	15-Sep-26 12:00 A	0.00	0.00	0.00	100%	100%	-43
PG-T-PR-LL-EL-MS-80	Fire Alarm System Materials(Completed)	35	11-May-26 08:00	25-Jun-26 10:00	11-May-26 08:00 A	24-Jun-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-T-PR-LL-EL-MS-80_R	Fire Alarm System Materials(Remaining)	10	25-Jun-26 08:00	06-Jul-26 17:00	27-Aug-26 08:00 A	15-Sep-26 12:00 A	0.00	0.00	0.00	100%	100%	-7
SHORT LEAD ITEMS		28	17-Feb-26 08:00	28-Mar-26 10:00	17-Feb-26 08:00 A	26-Mar-26 17:00 A	0.00	0.00	0.00	0%	0%	0
EXTERNAL / LANDSCAPE WORK		23	17-Feb-26 08:00	17-Mar-26 10:00	17-Feb-26 08:00 A	16-Mar-26 17:00 A	0.00	0.00	0.00	0%	0%	0
PG-T-PR-SL-LS-MS-10	Backfilling Materials	23	17-Feb-26 08:00	17-Mar-26 10:00	17-Feb-26 08:00 A	16-Mar-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-T-PR-SL-LS-MS-20	Interlock tiles	4	12-Mar-26 08:00	17-Mar-26 10:00	12-Mar-26 08:00 A	16-Mar-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-T-PR-SL-LS-MS-30	Compacted Natural Ground Soil	20	21-Feb-26 08:00	17-Mar-26 10:00	21-Feb-26 08:00 A	16-Mar-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-T-PR-SL-LS-MS-40	Curb Stone	7	09-Mar-26 08:00	17-Mar-26 10:00	09-Mar-26 08:00 A	16-Mar-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-T-PR-SL-LS-MS-50	Thermoplastic pavement road marking	4	12-Mar-26 08:00	17-Mar-26 10:00	12-Mar-26 08:00 A	16-Mar-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-T-PR-SL-LS-MS-60	Traffic Signages	9	07-Mar-26 08:00	17-Mar-26 10:00	07-Mar-26 08:00 A	16-Mar-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-T-PR-SL-LS-MS-70	Tiees	4	12-Mar-26 08:00	17-Mar-26 10:00	12-Mar-26 08:00 A	16-Mar-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-T-PR-SL-LS-MS-80	Lawn	4	12-Mar-26 08:00	17-Mar-26 10:00	12-Mar-26 08:00 A	16-Mar-26 17:00 A	0.00	0.00	0.00	100%	100%	0
CONCRETE WORK		28	17-Feb-26 08:00	28-Mar-26 10:00	17-Feb-26 08:00 A	26-Mar-26 17:00 A	0.00	0.00	0.00	0%	0%	0
PG-T-PR-SL-CO-MS-10	Steel Rebar	17	17-Feb-26 08:00	10-Mar-26 10:00	17-Feb-26 08:00 A	09-Mar-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-T-PR-SL-CO-MS-20	Concrete	13	23-Feb-26 08:00	10-Mar-26 10:00	23-Feb-26 08:00 A	09-Mar-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-T-PR-SL-CO-MS-30	Screed	10	11-Mar-26 08:00	28-Mar-26 10:00	11-Mar-26 08:00 A	26-Mar-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-T-PR-SL-CO-MS-40	CMU Block	19	01-Mar-26 08:00	28-Mar-26 10:00	01-Mar-26 08:00 A	26-Mar-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-T-PR-SL-CO-MS-50	Concrete Repair & Protection Materials	19	01-Mar-26 08:00	28-Mar-26 10:00	01-Mar-26 08:00 A	26-Mar-26 17:00 A	0.00	0.00	0.00	100%	100%	0
ARCHITECTURAL & FINISHES WORK		4	10-Mar-26 08:00	15-Mar-26 10:00	10-Mar-26 08:00 A	14-Mar-26 17:00 A	0.00	0.00	0.00	0%	0%	0
PG-T-PR-SL-AR-MS-10	Ceramic tiles	4	10-Mar-26 08:00	15-Mar-26 10:00	10-Mar-26 08:00 A	14-Mar-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-T-PR-SL-AR-MS-100	Specialities Materials (Toilet accessories, lockers, logo, etc)	4	10-Mar-26 08:00	15-Mar-26 10:00	10-Mar-26 08:00 A	14-Mar-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-T-PR-SL-AR-MS-110	Waterproofing System Materials	4	10-Mar-26 08:00	15-Mar-26 10:00	10-Mar-26 08:00 A	14-Mar-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-T-PR-SL-AR-MS-20	Anti-slip Granite tiles	4	10-Mar-26 08:00	15-Mar-26 10:00	10-Mar-26 08:00 A	14-Mar-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-T-PR-SL-AR-MS-30	Epoxy Paint	4	10-Mar-26 08:00	15-Mar-26 10:00	10-Mar-26 08:00 A	14-Mar-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-T-PR-SL-AR-MS-40	Cement Plaster	4	10-Mar-26 08:00	15-Mar-26 10:00	10-Mar-26 08:00 A	14-Mar-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-T-PR-SL-AR-MS-50	Acrylic Paint	4	10-Mar-26 08:00	15-Mar-26 10:00	10-Mar-26 08:00 A	14-Mar-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-T-PR-SL-AR-MS-60	Stone Cladding	4	10-Mar-26 08:00	15-Mar-26 10:00	10-Mar-26 08:00 A	14-Mar-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-T-PR-SL-AR-MS-70	Phenolic Partition	4	10-Mar-26 08:00	15-Mar-26 10:00	10-Mar-26 08:00 A	14-Mar-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-T-PR-SL-AR-MS-80	Glass Partition	4	10-Mar-26 08:00	15-Mar-26 10:00	10-Mar-26 08:00 A	14-Mar-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-T-PR-SL-AR-MS-90	Gypsum Boards	4	10-Mar-26 08:00	15-Mar-26 10:00	10-Mar-26 08:00 A	14-Mar-26 17:00 A	0.00	0.00	0.00	100%	100%	0
METAL WORK		9	07-Mar-26 08:00	17-Mar-26 10:00	07-Mar-26 08:00 A	16-Mar-26 17:00 A	0.00	0.00	0.00	0%	0%	0
PG-T-PR-SL-MT-MS-10	Galvanized Steel Ladder	4	12-Mar-26 08:00	17-Mar-26 10:00	12-Mar-26 08:00 A	16-Mar-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-T-PR-SL-MT-MS-20	Galvanized Steel Roof Scupper	9	07-Mar-26 08:00	17-Mar-26 10:00	07-Mar-26 08:00 A	16-Mar-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-T-PR-SL-MT-MS-30	Galvanized Steel Cover with frame	9	07-Mar-26 08:00	17-Mar-26 10:00	07-Mar-26 08:00 A	16-Mar-26 17:00 A	0.00	0.00	0.00	100%	100%	0
HVAC WORK		19	23-Feb-26 08:00	17-Mar-26 10:00	23-Feb-26 08:00 A	16-Mar-26 17:00 A	0.00	0.00	0.00	0%	0%	0
PG-T-PR-SL-AC-MS-10	Split Air Conditioning Unit	19	23-Feb-26 08:00	17-Mar-26 10:00	23-Feb-26 08:00 A	16-Mar-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-T-PR-SL-AC-MS-20	Air Duct	15	28-Feb-26 08:00	17-Mar-26 10:00	28-Feb-26 08:00 A	16-Mar-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-T-PR-SL-AC-MS-30	Diffusers and Grills	11	04-Mar-26 08:00	17-Mar-26 10:00	04-Mar-26 08:00 A	16-Mar-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-T-PR-SL-AC-MS-40	Exhaust fans	11	04-Mar-26 08:00	17-Mar-26 10:00	04-Mar-26 08:00 A	16-Mar-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PLUMBING WORK		4	12-Mar-26 08:00	17-Mar-26 10:00	12-Mar-26 08:00 A	16-Mar-26 17:00 A	0.00	0.00	0.00	0%	0%	0
PG-T-PR-SL-PB-MS-10	PPR Pipes & Valves	4	12-Mar-26 08:00	17-Mar-26 10:00	12-Mar-26 08:00 A	16-Mar-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-T-PR-SL-PB-MS-20	UPCV Pipes	4	12-Mar-26 08:00	17-Mar-26 10:00	12-Mar-26 08:00 A	16-Mar-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-T-PR-SL-PB-MS-30	Sanitary Drainage Fixtures	4	12-Mar-26 08:00	17-Mar-26 10:00	12-Mar-26 08:00 A	16-Mar-26 17:00 A	0.00	0.00	0.00	100%	100%	0
IRRIGATION WORK		4	12-Mar-26 08:00	17-Mar-26 10:00	12-Mar-26 08:00 A	16-Mar-26 17:00 A	0.00	0.00	0.00	0%	0%	0
PG-T-PR-SL-IR-MS-10	Gate Valve including valve box	4	12-Mar-26 08:00	17-Mar-26 10:00	12-Mar-26 08:00 A	16-Mar-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-T-PR-SL-IR-MS-20	Bubblers and Spreyers	4	12-Mar-26 08:00	17-Mar-26 10:00	12-Mar-26 08:00 A	16-Mar-26 17:00 A	0.00	0.00	0.00	100%	100%	0
ELECTRICAL WORK		4	12-Mar-26 08:00	17-Mar-26 10:00	12-Mar-26 08:00 A	16-Mar-26 17:00 A	0.00	0.00	0.00	0%	0%	0
PG-T-PR-SL-EL-MS-10	Wiring Devices Materials	4	12-Mar-26 08:00	17-Mar-26 10:00	12-Mar-26 08:00 A	16-Mar-26 17:00 A	0.00	0.00	0.00	100%	100%	0
FIRE FIGHTING WORK		4	12-Mar-26 08:00	17-Mar-26 10:00	12-Mar-26 08:00 A	16-Mar-26 17:00 A	0.00	0.00	0.00	0%	0%	0
PG-T-PR-SL-FF-MS-10	Fire Extinguishers	4	12-Mar-26 08:00	17-Mar-26 10:00	12-Mar-26 08:00 A	16-Mar-26 17:00 A	0.00	0.00	0.00	100%	100%	0
MATERIAL APPROVALS		160	21-Feb-26 08:00	13-Jul-26 17:00	21-Feb-26 08:00 A	17-Sep-26 11:12 A	340,734.03	340,734.03	340,734.03	100%	100%	-66
LONG LEAD ITEMS		157	25-Feb-26 08:00	13-Jul-26 17:00	25-Feb-26 08:00 A	17-Sep-26 11:12 A	284,659.98	284,659.98	284,659.98	100%	100%	-66
EXTERNAL / LANDSCAPE WORK		56	25-Feb-26 08:00	05-May-26 17:00	25-Feb-26 08:00 A	05-May-26 17:00 A	15,425.28	15,425.28	15,425.28	100%	100%	0
PG-T-PR-LL-LS-MA-10	Bike and Walk Path Materials	41	15-Mar-26 08:00	05-May-26 17:00	15-Mar-26 08:00 A	05-May-26 17:00 A	9,027.00	9,027.00	9,027.00	100%	100%	0
PG-T-PR-LL-LS-MA-20	Benches, Seats (Rectangular & Circular)	56	25-Feb-26 08:00	05-May-26 17:00	25-Feb-26 08:00 A	05-May-26 17:00 A	3,869.07	3,869.07	3,869.07	100%	100%	0
PG-T-PR-LL-LS-MA-30	Fence, gates and accessories	43	12-Mar-26 08:00	05-May-26 17:00	12-Mar-26 08:00 A	05-May-26 17:00 A	2,529.21	2,529.21	2,529.21	100%	100%	0
SPORTS & RECREATIONAL FACILITIES WORK		119	02-Mar-26 08:00	11-Jul-26 17:00	02-Mar-26 08:00 A	03-Sep-26 17:00 A	238,773.54	238,773.54	238,773.54	100%	100%	-47
PG-T-PR-LL-SPMA-10	Football Playground Materials (Flooring, goal post, nets, paints, etc)	42	14-Mar-26 08:00	05-May-26 17:00	14-Mar-26 08:00 A	05-May-26 17:00 A	13,051.50	13,051.50	13,051.50	100%	100%	0
PG-T-PR-LL-SPMA-20	Basketball Playground Materials (Flooring, basketball poll, nets, paints,	42	14-Mar-26 08:00	05-May-26 17:00	14-Mar-26 08:00 A	05-May-26 17:00 A	2,256.00	2,256.00	2,256.00	100%	100%	0
PG-T-PR-LL-SPMA-30	Padel Playground Materials (Flooring, fence, tempered glass, etc)	42	14-Mar-26 08:00	05-May-26 17:00	14-Mar-26 08:00 A	05-May-26 17:00 A	5,950.80	5,950.80	5,950.80	100%	100%	0
PG-T-PR-LL-SPMA-40	Tartan Floor	43	12-Mar-26 08:00	05-May-26 17:00	12-Mar-26 08:00 A	05-May-26 17:00 A	8,775.00	8,775.00	8,775.00	100%	100%	0
PG-T-PR-LL-SPMA-50	Air Dome Materials(Completed)	91	02-Mar-26 08:00	24-Jun-26 17:00	02-Mar-26 08:00 A	24-Jun-26 17:00 A	62,622.07	62,622.07	62,622.07	100%	100%	0
PG-T-PR-LL-SPMA-50_R	Air Dome Materials(Remaining)	5	06-Jul-26 08:00	11-Jul-26 17:00	09-Jul-26 08:00 A	03-Sep-26 17:00 A	146,118.17	146,118.17	146,118.17	100%	100%	-44
CONCRETE WORK		38	11-Mar-26 08:00	28-Apr-26 17:00	11-Mar-26 08:00 A	28-Apr-26 17:00 A	1,417.50	1,417.50	1,417.50	100%	100%	0
PG-T-PR-LL-CO-MA-10	Autoclaved Aerated Panel	38	11-Mar-26 08:00	28-Apr-26 17:00	11-Mar-26 08:00 A	28-Apr-26 17:00 A	1,417.50	1,417.50	1,417.50	100%	100%	0
METAL WORK		42	15-Mar-26 08:00	06-May-26 17:00	15-Mar-26 08:00 A	06-May-26 17:00 A	889.23	889.23	889.23	100%	100%	0

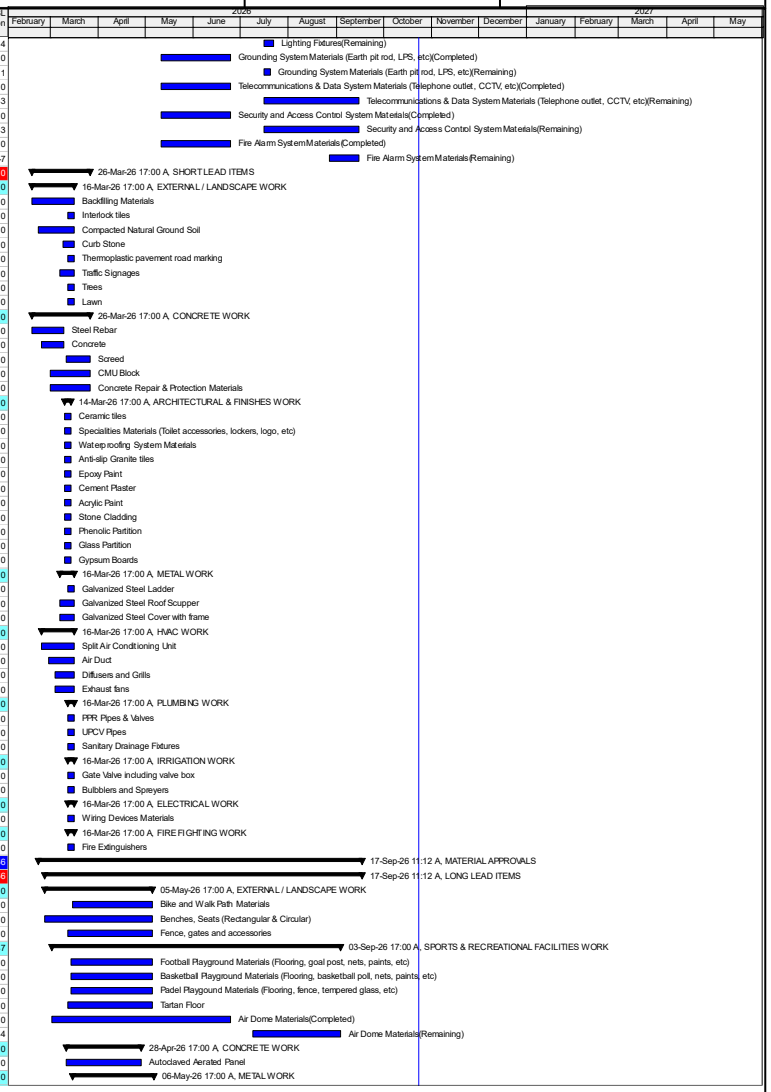


Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining W...
Milestone
summary

Baseline Schedule Rev.00

PLAYGROUNDS INITIATIVE - QASSIM, HAIL & TABUK - 25-Oct-2026

Activity ID	Activity Name	O.D	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Schedule % Complete	Performance % Complete	Variance - BL Project Duration
PG-T-PR-LL-MT-MA-10	Metal Doors	42	15-Mar-26 08:00	06-May-26 17:00	15-Mar-26 08:00 A	06-May-26 17:00 A	127.53	127.53	127.53	100%	100%	0
PG-T-PR-LL-MT-MA-20	Curtain Wall	42	15-Mar-26 08:00	06-May-26 17:00	15-Mar-26 08:00 A	06-May-26 17:00 A	761.70	761.70	761.70	100%	100%	0
PLUMBING WORK		42	15-Mar-26 08:00	06-May-26 17:00	15-Mar-26 08:00 A	06-May-26 17:00 A	3,553.95	3,553.95	3,553.95	100%	100%	0
PG-T-PR-LL-PB-MA-10	Booster Pump	42	15-Mar-26 08:00	06-May-26 17:00	15-Mar-26 08:00 A	06-May-26 17:00 A	1,818.30	1,818.30	1,818.30	100%	100%	0
PG-T-PR-LL-PB-MA-20	GRP Sectional Panel Water Tanks (4x3x3m)	38	24-Mar-26 08:00	06-May-26 17:00	24-Mar-26 08:00 A	06-May-26 17:00 A	1,735.65	1,735.65	1,735.65	100%	100%	0
IRRIGATION WORK		45	11-Mar-26 08:00	06-May-26 17:00	11-Mar-26 08:00 A	06-May-26 17:00 A	6,802.65	6,802.65	6,802.65	100%	100%	0
PG-T-PR-LL-IR-MA-10	HDPE Pipes	45	11-Mar-26 08:00	06-May-26 17:00	11-Mar-26 08:00 A	06-May-26 17:00 A	2,256.90	2,256.90	2,256.90	100%	100%	0
PG-T-PR-LL-IR-MA-20	Irrigation Control System	45	11-Mar-26 08:00	06-May-26 17:00	11-Mar-26 08:00 A	06-May-26 17:00 A	4,545.75	4,545.75	4,545.75	100%	100%	0
ELECTRICAL WORK		96	12-May-26 08:00	13-Jul-26 17:00	12-May-26 08:00 A	17-Sep-26 11:12 A	17,797.83	17,797.83	17,797.83	100%	100%	-56
PG-T-PR-LL-EL-MA-10	Main Distribution Board(Completed)	34	12-May-26 08:00	24-Jun-26 17:00	12-May-26 08:00 A	24-Jun-26 17:00 A	297.54	297.54	297.54	100%	100%	0
PG-T-PR-LL-EL-MA-10_R	Main Distribution Board(Remaining)	7	25-Jun-26 08:00	02-Jul-26 17:00	17-Jul-26 08:00 A	06-Aug-26 17:00 A	198.36	198.36	198.36	100%	100%	-11
PG-T-PR-LL-EL-MA-20	Power Panels (Pump, Street Light)(Completed)	34	12-May-26 08:00	24-Jun-26 17:00	12-May-26 08:00 A	24-Jun-26 17:00 A	238.03	238.03	238.03	100%	100%	0
PG-T-PR-LL-EL-MA-20_R	Power Panels (Pump, Street Light)(Remaining)	7	25-Jun-26 08:00	02-Jul-26 17:00	17-Jul-26 08:00 A	06-Aug-26 17:00 A	158.69	158.69	158.69	100%	100%	-11
PG-T-PR-LL-EL-MA-30	Site Lighting Poles(Completed)	34	12-May-26 08:00	24-Jun-26 17:00	12-May-26 08:00 A	24-Jun-26 17:00 A	6,962.11	6,962.11	6,962.11	100%	100%	0
PG-T-PR-LL-EL-MA-30_R	Site Lighting Poles(Remaining)	7	25-Jun-26 08:00	02-Jul-26 17:00	17-Jul-26 08:00 A	06-Aug-26 17:00 A	4,641.41	4,641.41	4,641.41	100%	100%	-11
PG-T-PR-LL-EL-MA-40	Lighting Fixtures(Completed)	34	12-May-26 08:00	24-Jun-26 17:00	12-May-26 08:00 A	24-Jun-26 17:00 A	769.70	769.70	769.70	100%	100%	0
PG-T-PR-LL-EL-MA-40_R	Lighting Fixtures(Remaining)	7	25-Jun-26 08:00	02-Jul-26 17:00	17-Jul-26 08:00 A	23-Jul-26 17:00 A	513.13	513.13	513.13	100%	100%	1
PG-T-PR-LL-EL-MA-50	Grounding System Materials (Earth pit rod, LPS, etc)(Completed)	34	12-May-26 08:00	24-Jun-26 17:00	12-May-26 08:00 A	24-Jun-26 17:00 A	602.51	602.51	602.51	100%	100%	0
PG-T-PR-LL-EL-MA-50_R	Grounding System Materials (Earth pit rod, LPS, etc)(Remaining)	2	12-Jul-26 08:00	13-Jul-26 17:00	22-Jul-26 08:00 A	28-Jul-26 17:00 A	401.68	401.68	401.68	100%	100%	-4
PG-T-PR-LL-EL-MA-60	Telecommunications & Data System Materials (Telephone outlet, CCTV,	34	12-May-26 08:00	24-Jun-26 17:00	12-May-26 08:00 A	24-Jun-26 17:00 A	587.63	587.63	587.63	100%	100%	0
PG-T-PR-LL-EL-MA-60_R	Telecommunications & Data System Materials (Telephone outlet, CCTV,	7	25-Jun-26 08:00	02-Jul-26 17:00	17-Jul-26 08:00 A	17-Sep-26 11:12 A	391.75	391.75	391.75	100%	100%	-46
PG-T-PR-LL-EL-MA-70	Security and Access Control System Materials(Completed)	34	12-May-26 08:00	24-Jun-26 17:00	12-May-26 08:00 A	24-Jun-26 17:00 A	743.94	743.94	743.94	100%	100%	0
PG-T-PR-LL-EL-MA-70_R	Security and Access Control System Materials(Remaining)	7	25-Jun-26 08:00	02-Jul-26 17:00	17-Jul-26 08:00 A	17-Sep-26 11:12 A	495.96	495.96	495.96	100%	100%	-46
PG-T-PR-LL-EL-MA-80	Fire Alarm System Materials(Completed)	34	12-May-26 08:00	24-Jun-26 17:00	12-May-26 08:00 A	24-Jun-26 17:00 A	477.23	477.23	477.23	100%	100%	0
PG-T-PR-LL-EL-MA-80_R	Fire Alarm System Materials(Remaining)	7	25-Jun-26 08:00	02-Jul-26 17:00	27-Aug-26 08:00 A	17-Sep-26 11:12 A	318.16	318.16	318.16	100%	100%	-11
SHORT LEAD ITEMS		25	21-Feb-26 08:00	26-Mar-26 17:00	21-Feb-26 08:00 A	26-Mar-26 17:00 A	56,074.05	56,074.05	56,074.05	100%	100%	0
EXTERNAL / LANDSCAPE WORK		25	21-Feb-26 08:00	26-Mar-26 17:00	21-Feb-26 08:00 A	26-Mar-26 17:00 A	38,542.29	38,542.29	38,542.29	100%	100%	0
PG-T-PR-SL-LS-MA-10	Backfilling Materials	25	21-Feb-26 08:00	26-Mar-26 17:00	21-Feb-26 08:00 A	26-Mar-26 17:00 A	10,125.00	10,125.00	10,125.00	100%	100%	0
PG-T-PR-SL-LS-MA-20	Interlock tiles	2	25-Mar-26 08:00	26-Mar-26 17:00	25-Mar-26 08:00 A	26-Mar-26 17:00 A	10,715.40	10,715.40	10,715.40	100%	100%	0
PG-T-PR-SL-LS-MA-30	Compacted Natural Ground Soil	22	25-Feb-26 08:00	26-Mar-26 17:00	25-Feb-26 08:00 A	26-Mar-26 17:00 A	1,287.00	1,287.00	1,287.00	100%	100%	0
PG-T-PR-SL-LS-MA-40	Curb Stone	2	25-Mar-26 08:00	26-Mar-26 17:00	25-Mar-26 08:00 A	26-Mar-26 17:00 A	10,339.80	10,339.80	10,339.80	100%	100%	0
PG-T-PR-SL-LS-MA-50	Thermoplastic pavement road marking	6	16-Mar-26 08:00	26-Mar-26 17:00	16-Mar-26 08:00 A	26-Mar-26 17:00 A	525.63	525.63	525.63	100%	100%	0
PG-T-PR-SL-LS-MA-60	Traffic Signages	11	10-Mar-26 08:00	26-Mar-26 17:00	10-Mar-26 08:00 A	26-Mar-26 17:00 A	198.36	198.36	198.36	100%	100%	0
PG-T-PR-SL-LS-MA-70	Trees	8	14-Mar-26 08:00	26-Mar-26 17:00	14-Mar-26 08:00 A	26-Mar-26 17:00 A	2,306.10	2,306.10	2,306.10	100%	100%	0
PG-T-PR-SL-LS-MA-80	Lawn	8	14-Mar-26 08:00	26-Mar-26 17:00	14-Mar-26 08:00 A	26-Mar-26 17:00 A	3,045.00	3,045.00	3,045.00	100%	100%	0
CONCRETE WORK		24	23-Feb-26 08:00	26-Mar-26 17:00	23-Feb-26 08:00 A	26-Mar-26 17:00 A	1,609.47	1,609.47	1,609.47	100%	100%	0
PG-T-PR-SL-CO-MA-10	Steel Rebar	14	23-Feb-26 08:00	10-Mar-26 17:00	23-Feb-26 08:00 A	10-Mar-26 17:00 A	476.82	476.82	476.82	100%	100%	0
PG-T-PR-SL-CO-MA-20	Concrete	9	01-Mar-26 08:00	10-Mar-26 17:00	01-Mar-26 08:00 A	10-Mar-26 17:00 A	518.85	518.85	518.85	100%	100%	0
PG-T-PR-SL-CO-MA-30	Screed	1	26-Mar-26 08:00	26-Mar-26 17:00	26-Mar-26 08:00 A	26-Mar-26 17:00 A	117.60	117.60	117.60	100%	100%	0
PG-T-PR-SL-CO-MA-40	CMU Block	15	05-Mar-26 08:00	26-Mar-26 17:00	05-Mar-26 08:00 A	26-Mar-26 17:00 A	124.20	124.20	124.20	100%	100%	0
PG-T-PR-SL-CO-MA-50	Concrete Repair & Protection Materials	15	05-Mar-26 08:00	26-Mar-26 17:00	05-Mar-26 08:00 A	26-Mar-26 17:00 A	372.00	372.00	372.00	100%	100%	0
ARCHITECTURAL & FINISHES WORK		2	15-Mar-26 08:00	16-Mar-26 17:00	15-Mar-26 08:00 A	16-Mar-26 17:00 A	7,931.55	7,931.55	7,931.55	100%	100%	0
PG-T-PR-SL-AR-MA-10	Ceramic tiles	2	15-Mar-26 08:00	16-Mar-26 17:00	15-Mar-26 08:00 A	16-Mar-26 17:00 A	571.95	571.95	571.95	100%	100%	0
PG-T-PR-SL-AR-MA-100	Specialities Materials (Toilet accessories, lockers, logo, etc)	2	15-Mar-26 08:00	16-Mar-26 17:00	15-Mar-26 08:00 A	16-Mar-26 17:00 A	2,262.87	2,262.87	2,262.87	100%	100%	0
PG-T-PR-SL-AR-MA-110	Waterproofing System Materials	2	15-Mar-26 08:00	16-Mar-26 17:00	15-Mar-26 08:00 A	16-Mar-26 17:00 A	544.20	544.20	544.20	100%	100%	0
PG-T-PR-SL-AR-MA-20	Anti-slip Granite tiles	2	15-Mar-26 08:00	16-Mar-26 17:00	15-Mar-26 08:00 A	16-Mar-26 17:00 A	535.50	535.50	535.50	100%	100%	0
PG-T-PR-SL-AR-MA-30	Epoxy Paint	2	15-Mar-26 08:00	16-Mar-26 17:00	15-Mar-26 08:00 A	16-Mar-26 17:00 A	111.18	111.18	111.18	100%	100%	0
PG-T-PR-SL-AR-MA-40	Cement Plaster	2	15-Mar-26 08:00	16-Mar-26 17:00	15-Mar-26 08:00 A	16-Mar-26 17:00 A	221.37	221.37	221.37	100%	100%	0
PG-T-PR-SL-AR-MA-50	Acrylic Paint	2	15-Mar-26 08:00	16-Mar-26 17:00	15-Mar-26 08:00 A	16-Mar-26 17:00 A	147.90	147.90	147.90	100%	100%	0
PG-T-PR-SL-AR-MA-60	Stone Cladding	2	15-Mar-26 08:00	16-Mar-26 17:00	15-Mar-26 08:00 A	16-Mar-26 17:00 A	1,852.20	1,852.20	1,852.20	100%	100%	0
PG-T-PR-SL-AR-MA-70	Phenolic Partition	2	15-Mar-26 08:00	16-Mar-26 17:00	15-Mar-26 08:00 A	16-Mar-26 17:00 A	1,340.40	1,340.40	1,340.40	100%	100%	0
PG-T-PR-SL-AR-MA-80	Glass Partition	2	15-Mar-26 08:00	16-Mar-26 17:00	15-Mar-26 08:00 A	16-Mar-26 17:00 A	155.40	155.40	155.40	100%	100%	0
PG-T-PR-SL-AR-MA-90	Gypsum Boards	2	15-Mar-26 08:00	16-Mar-26 17:00	15-Mar-26 08:00 A	16-Mar-26 17:00 A	188.58	188.58	188.58	100%	100%	0
METAL WORK		10	11-Mar-26 08:00	26-Mar-26 17:00	11-Mar-26 08:00 A	26-Mar-26 17:00 A	478.89	478.89	478.89	100%	100%	0
PG-T-PR-SL-MT-MA-10	Galvanized Steel Ladder	7	15-Mar-26 08:00	26-Mar-26 17:00	15-Mar-26 08:00 A	26-Mar-26 17:00 A	361.86	361.86	361.86	100%	100%	0
PG-T-PR-SL-MT-MA-20	Galvanized Steel Roof Scupper	10	11-Mar-26 08:00	26-Mar-26 17:00	11-Mar-26 08:00 A	26-Mar-26 17:00 A	31.32	31.32	31.32	100%	100%	0
PG-T-PR-SL-MT-MA-30	Galvanized Steel Cover with frame	10	11-Mar-26 08:00	26-Mar-26 17:00	11-Mar-26 08:00 A	26-Mar-26 17:00 A	85.71	85.71	85.71	100%	100%	0
HVAC WORK		20	28-Feb-26 08:00	26-Mar-26 17:00	28-Feb-26 08:00 A	26-Mar-26 17:00 A	606.36	606.36	606.36	100%	100%	0
PG-T-PR-SL-AC-MA-10	Split Air Conditioning Unit	20	28-Feb-26 08:00	26-Mar-26 17:00	28-Feb-26 08:00 A	26-Mar-26 17:00 A	309.93	309.93	309.93	100%	100%	0
PG-T-PR-SL-AC-MA-20	Air Duct	16	04-Mar-26 08:00	26-Mar-26 17:00	04-Mar-26 08:00 A	26-Mar-26 17:00 A	156.00	156.00	156.00	100%	100%	0
PG-T-PR-SL-AC-MA-30	Diffusers and Grills	2	25-Mar-26 08:00	26-Mar-26 17:00	25-Mar-26 08:00 A	26-Mar-26 17:00 A	74.31	74.31	74.31	100%	100%	0
PG-T-PR-SL-AC-MA-40	Exhaust fans	2	25-Mar-26 08:00	26-Mar-26 17:00	25-Mar-26 08:00 A	26-Mar-26 17:00 A	66.12	66.12	66.12	100%	100%	0
PLUMBING WORK		2	25-Mar-26 08:00	26-Mar-26 17:00	25-Mar-26 08:00 A	26-Mar-26 17:00 A	3,147.03	3,147.03	3,147.03	100%	100%	0
PG-T-PR-SL-PB-MA-10	PPR Pipes & Valves	2	25-Mar-26 08:00	26-Mar-26 17:00	25-Mar-26 08:00 A	26-Mar-26 17:00 A	265.20	265.20	265.20	100%	100%	0
PG-T-PR-SL-PB-MA-20	UPCV Pipes	2	25-Mar-26 08:00	26-Mar-26 17:00	25-Mar-26 08:00 A	26-Mar-26 17:00 A	335.19	335.19	335.19	100%	100%	0
PG-T-PR-SL-PB-MA-30	Sanitary Drainage Fixtures	2	25-Mar-26 08:00	26-Mar-26 17:00	25-Mar-26 08:00 A	26-Mar-26 17:00 A	2,546.64	2,546.64	2,546.64	100%	100%	0
IRRIGATION WORK		2	25-Mar-26 08:00	26-Mar-26 17:00	25-Mar-26 08:00 A	26-Mar-26 17:00 A	3,328.23	3,328.23	3,328.23	100%	100%	0
PG-T-PR-SL-IR-MA-10	Gate Valve including valve box	2	25-Mar-26 08:00	26-Mar-26 17:00	25-Mar-26 08:00 A	26-Mar-26 17:00 A	413.28	413.28	413.28	100%	100%	0
PG-T-PR-SL-IR-MA-20	Bubblers and Spreyers	2	25-Mar-26 08:00	26-Mar-26 17:00	25-Mar-26 08:00 A	26-Mar-26 17:00 A	2,914.95	2,914.95	2,914.95	100%	100%	0
ELECTRICAL WORK		2	25-Mar-26 08:00	26-Mar-26 17:00	25-Mar-26 08:00 A	26-Mar-26 17:00 A	407.52	407.52	407.52	100%	100%	0
PG-T-PR-SL-EL-MA-10	Wiring Devices Materials	2	25-Mar-26 08:00	26-Mar-26 17:00	25-Mar-26 08:00 A	26-Mar-26 17:00 A	407.52	407.52	407.52	100%	100%	0
FIRE FIGHTING WORK		2	25-Mar-26 08:00	26-Mar-26 17:00	25-Mar-26 08:00 A	26-Mar-26 17:00 A	22.71	22.71	22.71	100%	100%	0
PG-T-PR-SL-FF-MA-10	Fire Extinguishers	2	25-Mar-26 08:00	26-Mar-26 17:00	25-Mar-26 08:00 A	26-Mar-26 17:00 A	22.71	22.71	22.71	100%	100%	0

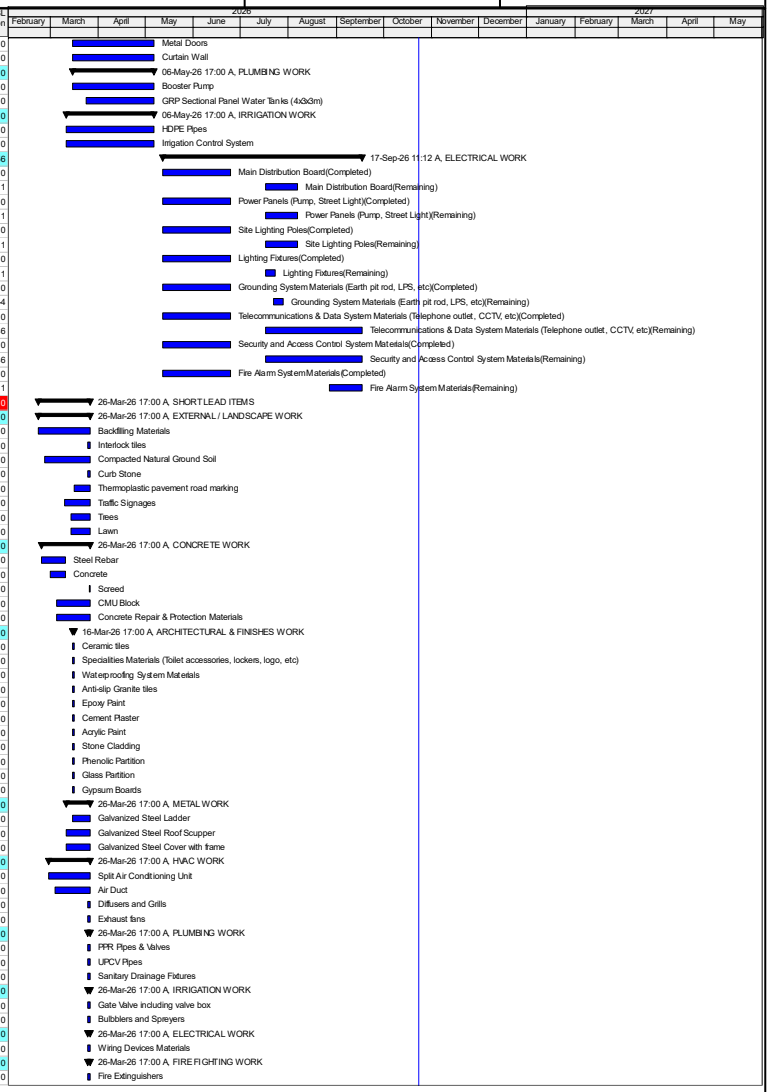


Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining W...
Milestone
summary

Baseline Schedule Rev.00

PLAYGROUNDS INITIATIVE - QASSIM, HAIL & TABUK - 25-Oct-2026

Activity ID	Activity Name	O.D	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Schedule % Complete	Performance % Complete	Variance - BL Project Duration
PROCUREMENT		201	26-Feb-26 08:00	27-Aug-26 17:00	26-Feb-26 08:00 A	27-Oct-26 12:48	3,066,606.27	2,662,683.45	3,066,606.27	100%	86.83%	-51
LONG LEAD ITEMS		194	07-Mar-26 08:00	27-Aug-26 17:00	07-Mar-26 08:00 A	27-Oct-26 12:48	2,561,939.82	2,161,684.91	2,561,939.82	100%	84.38%	-51
PURCHASE ORDER		157	07-Mar-26 08:00	16-Jul-26 17:00	07-Mar-26 08:00 A	10-Sep-26 17:00 A	0.00	0.00	0.00	0%	0%	48
EXTERNAL / LANDSCAPE WORK		49	07-Mar-26 08:00	07-May-26 10:00	07-Mar-26 08:00 A	06-May-26 17:00 A	0.00	0.00	0.00	0%	0%	0
PG-T-PR-LL-LS-PO-10	Bike and Walk Path Materials	34	29-Mar-26 08:00	07-May-26 10:00	29-Mar-26 08:00 A	06-May-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-T-PR-LL-LS-PO-20	Benches, Seats (Rectangular & Circular)	49	07-Mar-26 08:00	07-May-26 10:00	07-Mar-26 08:00 A	06-May-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-T-PR-LL-LS-PO-30	Fence, gates and accessories	36	26-Mar-26 08:00	07-May-26 10:00	26-Mar-26 08:00 A	06-May-26 17:00 A	0.00	0.00	0.00	100%	100%	0
SPORTS & RECREATIONAL FACILITIES WORK		119	26-Mar-26 08:00	16-Jul-26 17:00	26-Mar-26 08:00 A	10-Sep-26 17:00 A	0.00	0.00	0.00	0%	0%	48
PG-T-PR-LL-SPPO-10	Football Playground Materials (Flooring, goal post, nets, paints, etc)	35	28-Mar-26 08:00	07-May-26 10:00	28-Mar-26 08:00 A	06-May-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-T-PR-LL-SPPO-20	Basketball Playground Materials (Flooring, basketball poll, nets, paints,	35	28-Mar-26 08:00	07-May-26 10:00	28-Mar-26 08:00 A	06-May-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-T-PR-LL-SPPO-30	Padel Playgound Materials (Flooring, fence, tempered glass, etc)	35	28-Mar-26 08:00	07-May-26 10:00	28-Mar-26 08:00 A	06-May-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-T-PR-LL-SPPO-40	Tartan Floor	36	26-Mar-26 08:00	07-May-26 10:00	26-Mar-26 08:00 A	06-May-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-T-PR-LL-SPPO-50	Air Dome Materials	5	12-Jul-26 08:00	16-Jul-26 17:00	06-Aug-26 08:00 A	10-Sep-26 17:00 A	0.00	0.00	0.00	100%	100%	-26
CONCRETE WORK		39	18-Mar-26 08:00	07-May-26 10:00	18-Mar-26 08:00 A	06-May-26 17:00 A	0.00	0.00	0.00	0%	0%	0
PG-T-PR-LL-CO-PO-10	Autoclaved Aerated Panel	39	18-Mar-26 08:00	07-May-26 10:00	18-Mar-26 08:00 A	06-May-26 17:00 A	0.00	0.00	0.00	100%	100%	0
METAL WORK		38	24-Mar-26 08:00	07-May-26 10:00	24-Mar-26 08:00 A	06-May-26 17:00 A	0.00	0.00	0.00	0%	0%	0
PG-T-PR-LL-MT-PO-10	Metal Doors	38	24-Mar-26 08:00	07-May-26 10:00	24-Mar-26 08:00 A	06-May-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-T-PR-LL-MT-PO-20	Curtain Wall	38	24-Mar-26 08:00	07-May-26 10:00	24-Mar-26 08:00 A	06-May-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PLUMBING WORK		35	28-Mar-26 08:00	07-May-26 10:00	28-Mar-26 08:00 A	06-May-26 17:00 A	0.00	0.00	0.00	0%	0%	0
PG-T-PR-LL-PB-PO-10	Booster Pump	35	28-Mar-26 08:00	07-May-26 10:00	28-Mar-26 08:00 A	06-May-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-T-PR-LL-PB-PO-20	GRP Sectional Panel Water Tanks (4x3x3m)	33	30-Mar-26 08:00	07-May-26 10:00	30-Mar-26 08:00 A	06-May-26 17:00 A	0.00	0.00	0.00	100%	100%	0
IRRIGATION WORK		40	17-Mar-26 08:00	07-May-26 10:00	17-Mar-26 08:00 A	06-May-26 17:00 A	0.00	0.00	0.00	0%	0%	0
PG-T-PR-LL-IR-PO-10	HDPE Pipes	39	18-Mar-26 08:00	07-May-26 10:00	18-Mar-26 08:00 A	06-May-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-T-PR-LL-IR-PO-20	Irrigation Control System	40	17-Mar-26 08:00	07-May-26 10:00	17-Mar-26 08:00 A	06-May-26 17:00 A	0.00	0.00	0.00	100%	100%	0
ELECTRICAL WORK		105	11-May-26 08:00	16-Jul-26 17:00	11-May-26 08:00 A	10-Sep-26 09:36 A	0.00	0.00	0.00	0%	0%	47
PG-T-PR-LL-EL-PO-10	Main Distribution Board(Completed)	35	11-May-26 08:00	25-Jun-26 10:00	11-May-26 08:00 A	24-Jun-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-T-PR-LL-EL-PO-10_R	Main Distribution Board(Remaining)	8	04-Jul-26 08:00	12-Jul-26 17:00	26-Jul-26 08:00 A	10-Sep-26 09:36 A	0.00	0.00	0.00	100%	100%	32
PG-T-PR-LL-EL-PO-20	Power Panels (Pump, Street Light)(Completed)	35	11-May-26 08:00	25-Jun-26 10:00	11-May-26 08:00 A	24-Jun-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-T-PR-LL-EL-PO-20_R	Power Panels (Pump, Street Light)(Remaining)	8	04-Jul-26 08:00	12-Jul-26 17:00	26-Jul-26 08:00 A	10-Sep-26 09:36 A	0.00	0.00	0.00	100%	100%	32
PG-T-PR-LL-EL-PO-30	Site Lighting Poles(Completed)	35	11-May-26 08:00	25-Jun-26 10:00	11-May-26 08:00 A	24-Jun-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-T-PR-LL-EL-PO-30_R	Site Lighting Poles(Remaining)	8	04-Jul-26 08:00	12-Jul-26 17:00	26-Jul-26 08:00 A	10-Sep-26 09:36 A	0.00	0.00	0.00	100%	100%	32
PG-T-PR-LL-EL-PO-40	Lighting Fixtures(Completed)	35	11-May-26 08:00	25-Jun-26 10:00	11-May-26 08:00 A	24-Jun-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-T-PR-LL-EL-PO-40_R	Lighting Fixtures(Remaining)	8	04-Jul-26 08:00	12-Jul-26 17:00	23-Jul-26 08:00 A	10-Sep-26 09:36 A	0.00	0.00	0.00	100%	100%	34
PG-T-PR-LL-EL-PO-50	Grounding System Materials (Earth pit rod, LPS, etc)(Completed)	35	11-May-26 08:00	25-Jun-26 10:00	11-May-26 08:00 A	24-Jun-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-T-PR-LL-EL-PO-50_R	Grounding System Materials (Earth pit rod, LPS, etc)(Remaining)	3	14-Jul-26 08:00	16-Jul-26 17:00	26-Jul-26 08:00 A	10-Sep-26 09:36 A	0.00	0.00	0.00	100%	100%	37
PG-T-PR-LL-EL-PO-60	Telecommunications & Data System Materials (Telephone outlet, CCTV,	35	11-May-26 08:00	25-Jun-26 10:00	11-May-26 08:00 A	24-Jun-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-T-PR-LL-EL-PO-60_R	Telecommunications & Data System Materials (Telephone outlet, CCTV,	8	04-Jul-26 08:00	12-Jul-26 17:00	27-Aug-26 08:00 A	10-Sep-26 09:36 A	0.00	0.00	0.00	100%	100%	4
PG-T-PR-LL-EL-PO-70	Security and Access Control System Materials(Completed)	35	11-May-26 08:00	25-Jun-26 10:00	11-May-26 08:00 A	24-Jun-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-T-PR-LL-EL-PO-70_R	Security and Access Control System Materials(Remaining)	8	04-Jul-26 08:00	12-Jul-26 17:00	27-Aug-26 08:00 A	10-Sep-26 09:36 A	0.00	0.00	0.00	100%	100%	4
PG-T-PR-LL-EL-PO-80	Fire Alarm System Materials(Completed)	35	11-May-26 08:00	25-Jun-26 10:00	11-May-26 08:00 A	24-Jun-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-T-PR-LL-EL-PO-80_R	Fire Alarm System Materials(Remaining)	8	04-Jul-26 08:00	12-Jul-26 17:00	27-Aug-26 08:00 A	10-Sep-26 09:36 A	0.00	0.00	0.00	100%	100%	4
MANUFACTURE / FABRICATION		140	29-Apr-26 08:00	16-Aug-26 17:00	29-Apr-26 08:00 A	15-Oct-26 17:00 A	0.00	0.00	0.00	0%	0%	51
EXTERNAL / LANDSCAPE WORK		102	06-May-26 08:00	23-Jul-26 17:00	06-May-26 08:00 A	10-Sep-26 17:00 A	0.00	0.00	0.00	0%	0%	42
PG-T-PR-LL-LS-MF-10	Bike and Walk Path Materials(Completed)	39	06-May-26 08:00	25-Jun-26 10:00	06-May-26 08:00 A	24-Jun-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-T-PR-LL-LS-MF-10_R	Bike and Walk Path Materials(Remaining)	25	25-Jun-26 08:00	23-Jul-26 17:00	05-Aug-26 08:00 A	05-Sep-26 17:00 A	0.00	0.00	0.00	100%	100%	2
PG-T-PR-LL-LS-MF-20	Benches, Seats (Rectangular & Circular)(Completed)	39	06-May-26 08:00	25-Jun-26 10:00	06-May-26 08:00 A	24-Jun-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-T-PR-LL-LS-MF-20_R	Benches, Seats (Rectangular & Circular)(Remaining)	25	25-Jun-26 08:00	23-Jul-26 17:00	05-Aug-26 08:00 A	07-Sep-26 17:00 A	0.00	0.00	0.00	100%	100%	4
PG-T-PR-LL-LS-MF-30	Fence, gates and accessories(Completed)	39	06-May-26 08:00	25-Jun-26 10:00	06-May-26 08:00 A	24-Jun-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-T-PR-LL-LS-MF-30_R	Fence, gates and accessories(Remaining)	6	25-Jun-26 08:00	01-Jul-26 17:00	22-Jul-26 08:00 A	10-Sep-26 17:00 A	0.00	0.00	0.00	100%	100%	38
SPORTS & RECREATIONAL FACILITIES WORK		124	06-May-26 08:00	16-Aug-26 17:00	06-May-26 08:00 A	15-Oct-26 17:00 A	0.00	0.00	0.00	0%	0%	51
PG-T-PR-LL-SPMF-10	Football Playground Materials (Flooring, goal post, nets, paints,	39	06-May-26 08:00	25-Jun-26 10:00	06-May-26 08:00 A	24-Jun-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-T-PR-LL-SPMF-10_R	Football Playground Materials (Flooring, goal post, nets, paints,	25	25-Jun-26 08:00	23-Jul-26 17:00	05-Aug-26 08:00 A	02-Sep-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-T-PR-LL-SPMF-20	Basketball Playground Materials (Flooring, basketball poll, nets, paints,	39	06-May-26 08:00	25-Jun-26 10:00	06-May-26 08:00 A	24-Jun-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-T-PR-LL-SPMF-20_R	Basketball Playground Materials (Flooring, basketball poll, nets, paints,	25	25-Jun-26 08:00	23-Jul-26 17:00	05-Aug-26 08:00 A	04-Sep-26 17:00 A	0.00	0.00	0.00	100%	100%	1
PG-T-PR-LL-SPMF-30	Padel Playgound Materials (Flooring, fence, tempered glass,	39	06-May-26 08:00	25-Jun-26 10:00	06-May-26 08:00 A	24-Jun-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-T-PR-LL-SPMF-30_R	Padel Playgound Materials (Flooring, fence, tempered glass,	25	25-Jun-26 08:00	23-Jul-26 17:00	05-Aug-26 08:00 A	05-Sep-26 17:00 A	0.00	0.00	0.00	100%	100%	2
PG-T-PR-LL-SPMF-40	Tartan Floor(Completed)	39	06-May-26 08:00	25-Jun-26 10:00	06-May-26 08:00 A	24-Jun-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-T-PR-LL-SPMF-40_R	Tartan Floor(Remaining)	25	25-Jun-26 08:00	23-Jul-26 17:00	05-Aug-26 08:00 A	19-Sep-26 17:00 A	0.00	0.00	0.00	100%	100%	14
PG-T-PR-LL-SPMF-50	Air Dome Materials	26	18-Jul-26 08:00	16-Aug-26 17:00	27-Aug-26 08:00 A	15-Oct-26 17:00 A	0.00	0.00	0.00	100%	100%	16
CONCRETE WORK		64	29-Apr-26 08:00	30-Jun-26 17:00	29-Apr-26 08:00 A	02-Jul-26 17:00 A	0.00	0.00	0.00	0%	0%	2
PG-T-PR-LL-CO-MF-10	Autoclaved Aerated Panel(Completed)	45	29-Apr-26 08:00	25-Jun-26 10:00	29-Apr-26 08:00 A	24-Jun-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-T-PR-LL-CO-MF-10_R	Autoclaved Aerated Panel(Remaining)	5	25-Jun-26 08:00	30-Jun-26 17:00	01-Jul-26 08:00 A	02-Jul-26 17:00 A	0.00	0.00	0.00	100%	100%	3
METAL WORK		119	06-May-26 08:00	23-Jul-26 17:00	06-May-26 08:00 A	27-Sep-26 17:00 A	0.00	0.00	0.00	0%	0%	55
PG-T-PR-LL-MT-MF-10	Metal Doors(Completed)	39	06-May-26 08:00	25-Jun-26 10:00	06-May-26 08:00 A	24-Jun-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-T-PR-LL-MT-MF-10_R	Metal Doors(Remaining)	25	25-Jun-26 08:00	23-Jul-26 17:00	27-Aug-26 08:00 A	17-Sep-26 17:00 A	0.00	0.00	0.00	100%	100%	6
PG-T-PR-LL-MT-MF-20	Curtain Wall(Completed)	39	06-May-26 08:00	25-Jun-26 10:00	06-May-26 08:00 A	24-Jun-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-T-PR-LL-MT-MF-20_R	Curtain Wall(Remaining)	25	25-Jun-26 08:00	23-Jul-26 17:00	27-Aug-26 08:00 A	27-Sep-26 17:00 A	0.00	0.00	0.00	100%	100%	1
PLUMBING WORK		102	06-May-26 08:00	23-Jul-26 17:00	06-May-26 08:00 A	14-Sep-26 17:00 A	0.00	0.00	0.00	0%	0%	45
PG-T-PR-LL-PB-MF-10	Booster Pump(Completed)	39	06-May-26 08:00	25-Jun-26 10:00	06-May-26 08:00 A	24-Jun-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-T-PR-LL-PB-MF-10_R	Booster Pump(Remaining)	25	25-Jun-26 08:00	23-Jul-26 17:00	25-Jun-26 08:00 A	02-Jul-26 17:00 A	0.00	0.00	0.00	100%	100%	18
PG-T-PR-LL-PB-MF-20	GRP Sectional Panel Water Tanks (4x3x3m)(Completed)	39	06-May-26 08:00	25-Jun-26 10:00	06-May-26 08:00 A	24-Jun-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-T-PR-LL-PB-MF-20_R	GRP Sectional Panel Water Tanks (4x3x3m)(Remaining)	25	25-Jun-26 08:00	23-Jul-26 17:00	05-Aug-26 08:00 A	14-Sep-26 17:00 A	0.00	0.00	0.00	100%	100%	10
IRRIGATION WORK		99	06-May-26 08:00	30-Jun-26 17:00	06-May-26 08:00 A	21-Sep-26 12:24 A	0.00	0.00	0.00	0%	0%	71

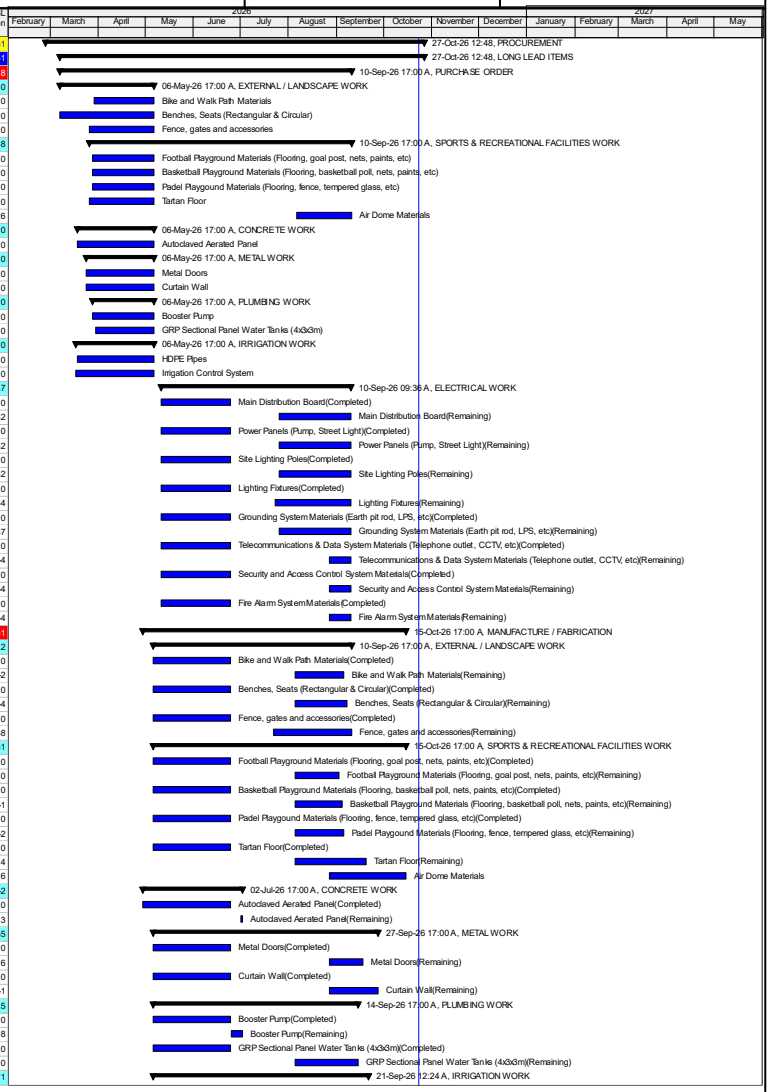


Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining W...
Milestone
summary

Baseline Schedule Rev.00

PLAYGROUNDS INITIATIVE - QASSIM, HAIL & TABUK - 25-Oct-2026

Activity ID	Activity Name	O.D	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Schedule % Complete	Performance % Complete	Variance - BL Project Duration
PG-T-PR-LL-IR-MF-10	HDPE Pipes(Completed)	39	06-May-26 08:00	25-Jun-26 10:00	06-May-26 08:00 A	24-Jun-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-T-PR-LL-IR-MF-10_R	HDPE Pipes(Remaining)	5	25-Jun-26 08:00	30-Jun-26 17:00	14-Aug-26 08:00 A	27-Aug-26 17:00 A	0.00	0.00	0.00	100%	100%	-7
PG-T-PR-LL-IR-MF-20	Irrigation Control System(Completed)	39	06-May-26 08:00	25-Jun-26 10:00	06-May-26 08:00 A	24-Jun-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-T-PR-LL-IR-MF-20_R	Irrigation Control System(Remaining)	5	25-Jun-26 08:00	30-Jun-26 17:00	27-Aug-26 08:00 A	21-Sep-26 12:24 A	0.00	0.00	0.00	100%	100%	-17
ELECTRICAL WORK		129	12-May-26 08:00	10-Aug-26 17:00	12-May-26 08:00 A	30-Sep-26 17:00 A	0.00	0.00	0.00	0%	0%	43
PG-T-PR-LL-EL-MF-10	Main Distribution Board(Completed)	34	12-May-26 08:00	25-Jun-26 10:00	12-May-26 08:00 A	24-Jun-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-T-PR-LL-EL-MF-10_R	Main Distribution Board(Remaining)	25	13-Jul-26 08:00	10-Aug-26 17:00	06-Aug-26 08:00 A	28-Sep-26 17:00 A	0.00	0.00	0.00	100%	100%	-20
PG-T-PR-LL-EL-MF-20	Power Panels (Pump, Street Light)(Completed)	34	12-May-26 08:00	25-Jun-26 10:00	12-May-26 08:00 A	24-Jun-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-T-PR-LL-EL-MF-20_R	Power Panels (Pump, Street Light)(Remaining)	25	13-Jul-26 08:00	10-Aug-26 17:00	06-Aug-26 08:00 A	26-Sep-26 17:00 A	0.00	0.00	0.00	100%	100%	-18
PG-T-PR-LL-EL-MF-30	Site Lighting Poles(Completed)	34	12-May-26 08:00	25-Jun-26 10:00	12-May-26 08:00 A	24-Jun-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-T-PR-LL-EL-MF-30_R	Site Lighting Poles(Remaining)	25	13-Jul-26 08:00	10-Aug-26 17:00	06-Aug-26 08:00 A	29-Sep-26 17:00 A	0.00	0.00	0.00	100%	100%	-21
PG-T-PR-LL-EL-MF-40	Lighting Fixtures(Completed)	34	12-May-26 08:00	25-Jun-26 10:00	12-May-26 08:00 A	24-Jun-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-T-PR-LL-EL-MF-40_R	Lighting Fixtures(Remaining)	25	13-Jul-26 08:00	10-Aug-26 17:00	23-Jul-26 08:00 A	30-Sep-26 17:00 A	0.00	0.00	0.00	100%	100%	-34
PG-T-PR-LL-EL-MF-50	Grounding System Materials (Earth pit rod, LPS, etc)(Completed)	34	12-May-26 08:00	25-Jun-26 10:00	12-May-26 08:00 A	24-Jun-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-T-PR-LL-EL-MF-50_R	Grounding System Materials (Earth pit rod, LPS, etc)(Remaining)	6	18-Jul-26 08:00	23-Jul-26 17:00	27-Aug-26 08:00 A	27-Sep-26 17:00 A	0.00	0.00	0.00	100%	100%	-20
PG-T-PR-LL-EL-MF-60	Telecommunications & Data System Materials (Telephone outlet, CCTV,	34	12-May-26 08:00	25-Jun-26 10:00	12-May-26 08:00 A	24-Jun-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-T-PR-LL-EL-MF-60_R	Telecommunications & Data System Materials (Telephone outlet, CCTV,	25	13-Jul-26 08:00	10-Aug-26 17:00	27-Aug-26 08:00 A	29-Sep-26 17:00 A	0.00	0.00	0.00	100%	100%	-3
PG-T-PR-LL-EL-MF-70	Security and Access Control System Materials(Completed)	34	12-May-26 08:00	25-Jun-26 10:00	12-May-26 08:00 A	24-Jun-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-T-PR-LL-EL-MF-70_R	Security and Access Control System Materials(Remaining)	25	13-Jul-26 08:00	10-Aug-26 17:00	27-Aug-26 08:00 A	30-Sep-26 17:00 A	0.00	0.00	0.00	100%	100%	-4
PG-T-PR-LL-EL-MF-80	Fire Alarm System Materials(Completed)	34	12-May-26 08:00	25-Jun-26 10:00	12-May-26 08:00 A	24-Jun-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-T-PR-LL-EL-MF-80_R	Fire Alarm System Materials(Remaining)	25	13-Jul-26 08:00	10-Aug-26 17:00	27-Aug-26 08:00 A	30-Sep-26 17:00 A	0.00	0.00	0.00	100%	100%	-4
DELIVERY TO SITE		146	06-May-26 08:00	27-Aug-26 17:00	06-May-26 08:00 A	27-Oct-26 12:48	2,561,939.82	2,161,684.91	2,561,939.82	100%	84.38%	-51
EXTERNAL / LANDSCAPE WORK		114	06-May-26 08:00	06-Aug-26 17:00	06-May-26 08:00 A	25-Oct-26 09:36	138,827.52	137,434.65	138,827.52	100%	99%	-66
PG-T-PR-LL-LS-DL-10	Bike and Walk Path Materials(Completed)	39	06-May-26 08:00	24-Jun-26 17:00	06-May-26 08:00 A	24-Jun-26 17:00 A	56,870.10	56,870.10	56,870.10	100%	100%	0
PG-T-PR-LL-LS-DL-10_R	Bike and Walk Path Materials(Remaining)	12	25-Jul-26 08:00	06-Aug-26 17:00	06-Aug-26 08:00 A	28-Sep-26 17:00 A	24,372.90	24,372.90	24,372.90	100%	100%	-33
PG-T-PR-LL-LS-DL-20	Benches, Seats (Rectangular & Circular)(Completed)	39	06-May-26 08:00	24-Jun-26 17:00	06-May-26 08:00 A	24-Jun-26 17:00 A	20,892.98	20,892.98	20,892.98	100%	100%	0
PG-T-PR-LL-LS-DL-20_R	Benches, Seats (Rectangular & Circular)(Remaining)	12	25-Jul-26 08:00	06-Aug-26 17:00	14-Aug-26 08:00 A	25-Oct-26 09:36	13,928.65	12,535.79	13,928.65	100%	90%	-48
PG-T-PR-LL-LS-DL-30	Fence, gates and accessories(Completed)	39	06-May-26 08:00	24-Jun-26 17:00	06-May-26 08:00 A	24-Jun-26 17:00 A	11,381.45	11,381.45	11,381.45	100%	100%	0
PG-T-PR-LL-LS-DL-30_R	Fence, gates and accessories(Remaining)	5	02-Jul-26 08:00	07-Jul-26 17:00	23-Jul-26 08:00 A	19-Sep-26 12:00 A	11,381.45	11,381.45	11,381.45	100%	100%	-45
SPORTS & RECREATIONAL FACILITIES WORK		129	06-May-26 08:00	27-Aug-26 17:00	06-May-26 08:00 A	25-Oct-26 17:00	2,148,961.86	1,759,714.44	2,148,961.86	100%	81.89%	-49
PG-T-PR-LL-SPDL-10	Football Playground Materials (Flooring, goal post, nets, paints,	39	06-May-26 08:00	24-Jun-26 17:00	06-May-26 08:00 A	24-Jun-26 17:00 A	58,731.75	58,731.75	58,731.75	100%	100%	0
PG-T-PR-LL-SPDL-10_R	Football Playground Materials (Flooring, goal post, nets, paints,	12	25-Jul-26 08:00	06-Aug-26 17:00	14-Aug-26 08:00 A	25-Oct-26 09:36	58,731.75	52,858.58	58,731.75	100%	90%	-48
PG-T-PR-LL-SPDL-20	Basketball Playground Materials (Flooring, basketball poll, nets, paints,	39	06-May-26 08:00	24-Jun-26 17:00	06-May-26 08:00 A	24-Jun-26 17:00 A	10,152.00	10,152.00	10,152.00	100%	100%	0
PG-T-PR-LL-SPDL-20_R	Basketball Playground Materials (Flooring, basketball poll, nets, paints,	12	25-Jul-26 08:00	06-Aug-26 17:00	14-Aug-26 08:00 A	25-Oct-26 09:36	10,152.00	9,136.80	10,152.00	100%	90%	-48
PG-T-PR-LL-SPDL-30	Padel Playgound Materials (Fence, tempered glass, etc)(Completed)	39	06-May-26 08:00	24-Jun-26 17:00	06-May-26 08:00 A	24-Jun-26 17:00 A	26,778.60	26,778.60	26,778.60	100%	100%	0
PG-T-PR-LL-SPDL-30_R	Padel Playgound Materials (Fence, tempered glass, etc)(Remaining)	12	25-Jul-26 08:00	06-Aug-26 17:00	14-Aug-26 08:00 A	25-Oct-26 09:36	26,778.60	24,100.74	26,778.60	100%	90%	-48
PG-T-PR-LL-SPDL-40	Tartan Floor(Completed)	39	06-May-26 08:00	24-Jun-26 17:00	06-May-26 08:00 A	24-Jun-26 17:00 A	39,487.50	39,487.50	39,487.50	100%	100%	0
PG-T-PR-LL-SPDL-40_R	Tartan Floor(Remaining)	12	25-Jul-26 08:00	06-Aug-26 17:00	06-Aug-26 08:00 A	25-Oct-26 09:36	39,487.50	35,538.75	39,487.50	100%	90%	-55
PG-T-PR-LL-SPDL-50	Air Dome Materials	10	17-Aug-26 08:00	27-Aug-26 17:00	22-Oct-26 08:00 A	25-Oct-26 17:00	1,878,662.16	1,502,929.73	1,878,662.16	100%	80%	7
CONCRETE WORK		63	06-May-26 08:00	06-Jul-26 17:00	06-May-26 08:00 A	05-Jul-26 17:00 A	12,757.50	12,757.50	12,757.50	100%	100%	1
PG-T-PR-LL-CO-DL-10	Autoclaved Aerated Panel(Completed)	39	06-May-26 08:00	24-Jun-26 17:00	06-May-26 08:00 A	24-Jun-26 17:00 A	8,930.25	8,930.25	8,930.25	100%	100%	0
PG-T-PR-LL-CO-DL-10_R	Autoclaved Aerated Panel(Remaining)	5	01-Jul-26 08:00	06-Jul-26 17:00	04-Jul-26 08:00 A	05-Jul-26 17:00 A	3,827.25	3,827.25	3,827.25	100%	100%	3
METAL WORK		131	06-May-26 08:00	06-Aug-26 17:00	06-May-26 08:00 A	27-Oct-26 12:48	8,003.07	6,974.78	8,003.07	100%	87.15%	-69
PG-T-PR-LL-MT-DL-10	Metal Doors(Completed)	39	06-May-26 08:00	24-Jun-26 17:00	06-May-26 08:00 A	24-Jun-26 17:00 A	573.89	573.89	573.89	100%	100%	0
PG-T-PR-LL-MT-DL-10_R	Metal Doors(Remaining)	12	25-Jul-26 08:00	06-Aug-26 17:00	27-Aug-26 08:00 A	15-Oct-26 17:00 A	573.89	573.89	573.89	100%	100%	-30
PG-T-PR-LL-MT-DL-20	Curtain Wall(Completed)	39	06-May-26 08:00	24-Jun-26 17:00	06-May-26 08:00 A	24-Jun-26 17:00 A	3,427.65	3,427.65	3,427.65	100%	100%	0
PG-T-PR-LL-MT-DL-20_R	Curtain Wall(Remaining)	12	25-Jul-26 08:00	06-Aug-26 17:00	27-Aug-26 08:00 A	27-Oct-26 12:48	3,427.65	2,399.36	3,427.65	100%	70%	-40
PLUMBING WORK		108	06-May-26 08:00	06-Aug-26 17:00	06-May-26 08:00 A	15-Oct-26 17:00 A	31,985.55	31,985.55	31,985.55	100%	100%	-59
PG-T-PR-LL-PB-DL-10	Booster Pump(Completed)	39	06-May-26 08:00	24-Jun-26 17:00	06-May-26 08:00 A	24-Jun-26 17:00 A	9,818.82	9,818.82	9,818.82	100%	100%	0
PG-T-PR-LL-PB-DL-10_R	Booster Pump(Remaining)	12	25-Jul-26 08:00	06-Aug-26 17:00	27-Aug-26 08:00 A	26-Sep-26 11:12 A	6,545.88	6,545.88	6,545.88	100%	100%	-12
PG-T-PR-LL-PB-DL-20	GRP Sectional Panel Water Tanks (4x3x3m)(Completed)	39	06-May-26 08:00	24-Jun-26 17:00	06-May-26 08:00 A	24-Jun-26 17:00 A	9,372.51	9,372.51	9,372.51	100%	100%	0
PG-T-PR-LL-PB-DL-20_R	GRP Sectional Panel Water Tanks (4x3x3m)(Remaining)	12	25-Jul-26 08:00	06-Aug-26 17:00	14-Aug-26 08:00 A	15-Oct-26 17:00 A	6,248.34	6,248.34	6,248.34	100%	100%	-41
IRRIGATION WORK		98	06-May-26 08:00	05-Jul-26 17:00	06-May-26 08:00 A	24-Oct-26 11:12	61,223.85	59,587.38	61,223.85	100%	97.33%	-93
PG-T-PR-LL-IR-DL-10	HDPE Pipes(Completed)	39	06-May-26 08:00	24-Jun-26 17:00	06-May-26 08:00 A	24-Jun-26 17:00 A	12,187.26	12,187.26	12,187.26	100%	100%	0
PG-T-PR-LL-IR-DL-10_R	HDPE Pipes(Remaining)	4	01-Jul-26 08:00	05-Jul-26 17:00	07-Aug-26 08:00 A	22-Sep-26 17:00 A	8,124.84	8,124.84	8,124.84	100%	100%	-36
PG-T-PR-LL-IR-DL-20	Irrigation Control System(Completed)	39	06-May-26 08:00	24-Jun-26 17:00	06-May-26 08:00 A	24-Jun-26 17:00 A	24,547.05	24,547.05	24,547.05	100%	100%	0
PG-T-PR-LL-IR-DL-20_R	Irrigation Control System(Remaining)	4	01-Jul-26 08:00	05-Jul-26 17:00	20-Aug-26 08:00 A	24-Oct-26 11:12	16,364.70	14,728.23	16,364.70	100%	90%	-50
ELECTRICAL WORK		140	13-May-26 08:00	24-Aug-26 17:00	13-May-26 08:00 A	25-Oct-26 15:24	160,180.47	153,230.61	160,180.47	100%	95.66%	-52
PG-T-PR-LL-EL-DL-10	Main Distribution Board(Completed)	33	13-May-26 08:00	24-Jun-26 17:00	13-May-26 08:00 A	24-Jun-26 17:00 A	2,677.86	2,677.86	2,677.86	100%	100%	0
PG-T-PR-LL-EL-DL-10_R	Main Distribution Board(Remaining)	12	11-Aug-26 08:00	24-Aug-26 17:00	14-Aug-26 08:00 A	25-Oct-26 09:36	1,785.24	1,606.72	1,785.24	100%	90%	-48
PG-T-PR-LL-EL-DL-20	Power Panels (Pump, Street Light)(Completed)	33	13-May-26 08:00	24-Jun-26 17:00	13-May-26 08:00 A	24-Jun-26 17:00 A	2,142.29	2,142.29	2,142.29	100%	100%	0
PG-T-PR-LL-EL-DL-20_R	Power Panels (Pump, Street Light)(Remaining)	12	11-Aug-26 08:00	24-Aug-26 17:00	14-Aug-26 08:00 A	25-Oct-26 09:36	1,428.19	1,285.37	1,428.19	100%	90%	-48
PG-T-PR-LL-EL-DL-30	Site Lighting Poles(Completed)	33	13-May-26 08:00	24-Jun-26 17:00	13-May-26 08:00 A	24-Jun-26 17:00 A	62,659.01	62,659.01	62,659.01	100%	100%	0
PG-T-PR-LL-EL-DL-30_R	Site Lighting Poles(Remaining)	12	11-Aug-26 08:00	24-Aug-26 17:00	14-Aug-26 08:00 A	25-Oct-26 09:36	41,772.67	37,595.40	41,772.67	100%	90%	-48
PG-T-PR-LL-EL-DL-40	Lighting Fixtures(Completed)	33	13-May-26 08:00	24-Jun-26 17:00	13-May-26 08:00 A	24-Jun-26 17:00 A	6,927.28	6,927.28	6,927.28	100%	100%	0
PG-T-PR-LL-EL-DL-40_R	Lighting Fixtures(Remaining)	12	11-Aug-26 08:00	24-Aug-26 17:00	14-Aug-26 08:00 A	25-Oct-26 09:36	4,618.19	4,156.37	4,618.19	100%	90%	-48
PG-T-PR-LL-EL-DL-50	Grounding System Materials (Earth pit rod, LPS, etc)(Completed)	33	13-May-26 08:00	24-Jun-26 17:00	13-May-26 08:00 A	24-Jun-26 17:00 A	5,422.63	5,422.63	5,422.63	100%	100%	0
PG-T-PR-LL-EL-DL-50_R	Grounding System Materials (Earth pit rod, LPS, etc)(Remaining)	4	25-Jul-26 08:00	28-Jul-26 17:00	14-Aug-26 08:00 A	24-Oct-26 11:12	3,615.08	3,253.58	3,615.08	100%	90%	-55
PG-T-PR-LL-EL-DL-60	Telecommunications & Data System Materials (Telephone outlet, CCTV,	33	13-May-26 08:00	24-Jun-26 17:00	13-May-26 08:00 A	24-Jun-26 17:00 A	5,288.65	5,288.65	5,288.65	100%	100%	0
PG-T-PR-LL-EL-DL-60_R	Telecommunications & Data System Materials (Telephone outlet, CCTV,	12	11-Aug-26 08:00	24-Aug-26 17:00	27-Aug-26 08:00 A	25-Oct-26 15:24	3,525.77	2,996.90	3,525.77	100%	85%	-38
PG-T-PR-LL-EL-DL-70	Security and Access Control System Materials(Completed)	33	13-May-26 08:00	24-Jun-26 17:00	13-May-26 08:00 A	24-Jun-26 17:00 A	6,695.46	6,695.46	6,695.46	100%	100%	0
PG-T-PR-LL-EL-DL-70_R	Security and Access Control System Materials(Remaining)	12	11-Aug-26 08:00	24-Aug-26 17:00	27-Aug-26 08:00 A	25-Oct-26 15:24	4,463.64	3,794.09	4,463.64	100%	85%	-38
PG-T-PR-LL-EL-DL-80	Fire Alarm System Materials(Completed)	33	13-May-26 08:00	24-Jun-26 17:00	13-May-26 08:00 A	24-Jun-26 17:00 A	4,295.11	4,295.11	4,295.11	100%	100%	0

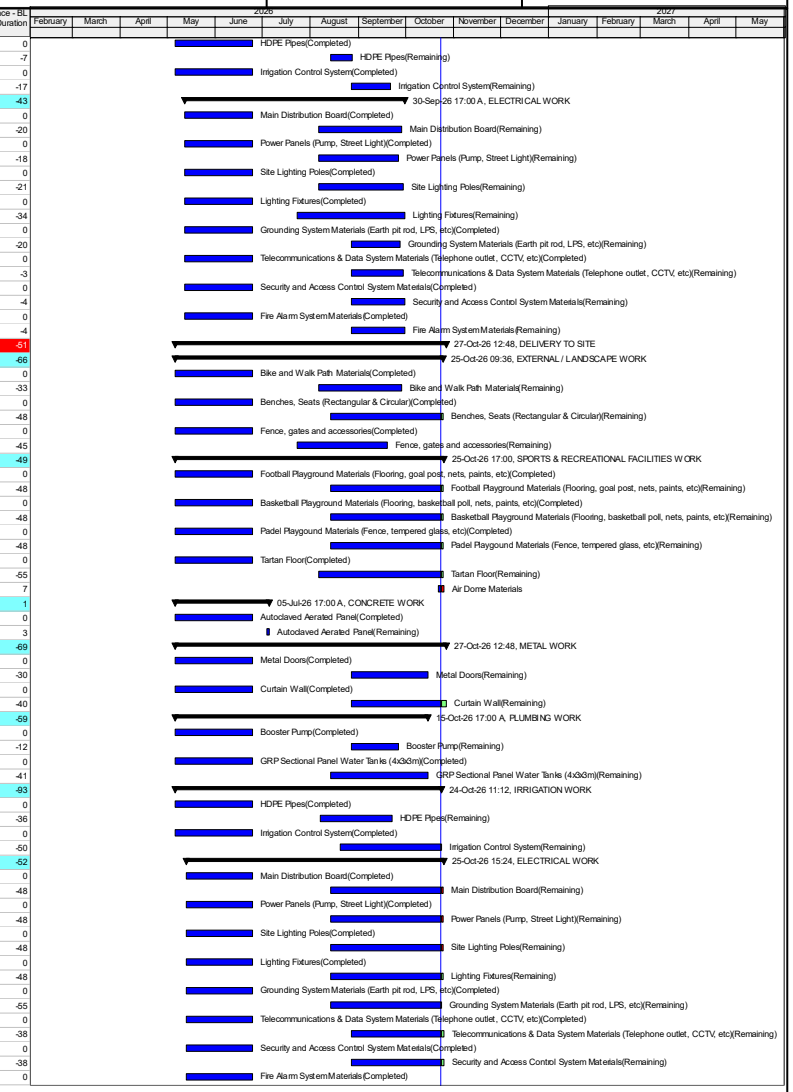


Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining W...
Milestone
summary

Baseline Schedule Rev.00

PLAYGROUNDS INITIATIVE - QASSIM, HAIL & TABUK - 25-Oct-2026

Activity ID	Activity Name	O.D	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Schedule % Complete	Performance % Complete	Variance - BL Project Duration
PG-T-PR-LL-EL-DL-80_R	Fire Alarm System Materials(Remaining)	12	11-Aug-26 08:00	24-Aug-26 17:00	27-Aug-26 08:00 A	25-Oct-26 15:24	2,863.40	2,433.89	2,863.40	100%	85%	-38
SHORT LEAD ITEMS		190	26-Feb-26 08:00	22-Jul-26 17:00	26-Feb-26 08:00 A	25-Oct-26 09:36	504,666.45	500,998.54	504,666.45	100%	99.27%	-79
PURCHASE ORDER		163	26-Feb-26 08:00	11-Jul-26 17:00	26-Feb-26 08:00 A	27-Aug-26 17:00 A	0.00	0.00	0.00	0%	0%	-41
EXTERNAL / LANDSCAPE WORK		163	26-Feb-26 08:00	11-Jul-26 17:00	26-Feb-26 08:00 A	27-Aug-26 17:00 A	0.00	0.00	0.00	0%	0%	-41
PG-T-PR-SL-LS-PO-10	Backfilling Materials	44	26-Feb-26 08:00	23-Apr-26 10:00	26-Feb-26 08:00 A	22-Apr-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-T-PR-SL-LS-PO-20	Interlock tiles	28	29-Mar-26 08:00	30-Apr-26 10:00	29-Mar-26 08:00 A	29-Apr-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-T-PR-SL-LS-PO-30	Compacted Natural Ground Soil	42	01-Mar-26 08:00	23-Apr-26 10:00	01-Mar-26 08:00 A	22-Apr-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-T-PR-SL-LS-PO-40	Curb Stone	23	04-Apr-26 08:00	30-Apr-26 10:00	04-Apr-26 08:00 A	29-Apr-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-T-PR-SL-LS-PO-50	Thermoplastic pavement road marking(Completed)	35	11-May-26 08:00	25-Jun-26 10:00	11-May-26 08:00 A	24-Jun-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-T-PR-SL-LS-PO-50_R	Thermoplastic pavement road marking(Remaining)	7	25-Jun-26 08:00	02-Jul-26 17:00	20-Aug-26 08:00 A	27-Aug-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-T-PR-SL-LS-PO-60	Traffic Signages(Completed)	35	11-May-26 08:00	25-Jun-26 10:00	11-May-26 08:00 A	24-Jun-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-T-PR-SL-LS-PO-60_R	Traffic Signages(Remaining)	7	04-Jul-26 08:00	11-Jul-26 17:00	20-Aug-26 08:00 A	27-Aug-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-T-PR-SL-LS-PO-70	Trees(Completed)	35	11-May-26 08:00	25-Jun-26 10:00	11-May-26 08:00 A	24-Jun-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-T-PR-SL-LS-PO-70_R	Trees(Remaining)	7	25-Jun-26 08:00	02-Jul-26 17:00	20-Aug-26 08:00 A	27-Aug-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-T-PR-SL-LS-PO-80	Lawn(Completed)	35	11-May-26 08:00	25-Jun-26 10:00	11-May-26 08:00 A	24-Jun-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-T-PR-SL-LS-PO-80_R	Lawn(Remaining)	7	25-Jun-26 08:00	02-Jul-26 17:00	20-Aug-26 08:00 A	27-Aug-26 17:00 A	0.00	0.00	0.00	100%	100%	0
CONCRETE WORK		41	02-Mar-26 08:00	23-Apr-26 10:00	02-Mar-26 08:00 A	22-Apr-26 17:00 A	0.00	0.00	0.00	0%	0%	0
PG-T-PR-SL-CO-PO-10	Steel Rebar	41	02-Mar-26 08:00	23-Apr-26 10:00	02-Mar-26 08:00 A	22-Apr-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-T-PR-SL-CO-PO-20	Concrete	36	08-Mar-26 08:00	23-Apr-26 10:00	08-Mar-26 08:00 A	22-Apr-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-T-PR-SL-CO-PO-30	Screed	23	28-Mar-26 08:00	23-Apr-26 10:00	28-Mar-26 08:00 A	22-Apr-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-T-PR-SL-CO-PO-40	CMU Block	33	11-Mar-26 08:00	23-Apr-26 10:00	11-Mar-26 08:00 A	22-Apr-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-T-PR-SL-CO-PO-50	Concrete Repair & Protection Materials	32	12-Mar-26 08:00	23-Apr-26 10:00	12-Mar-26 08:00 A	22-Apr-26 17:00 A	0.00	0.00	0.00	100%	100%	0
ARCHITECTURAL & FINISHES WORK		7	05-May-26 08:00	13-May-26 10:00	05-May-26 08:00 A	12-May-26 17:00 A	0.00	0.00	0.00	0%	0%	0
PG-T-PR-SL-AR-PO-10	Ceramic tiles	7	05-May-26 08:00	13-May-26 10:00	05-May-26 08:00 A	12-May-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-T-PR-SL-AR-PO-100	Specialities Materials (Toilet accessories, lockers, logo, etc)	7	05-May-26 08:00	13-May-26 10:00	05-May-26 08:00 A	12-May-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-T-PR-SL-AR-PO-110	Waterproofing System Materials	7	05-May-26 08:00	13-May-26 10:00	05-May-26 08:00 A	12-May-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-T-PR-SL-AR-PO-20	Anti-slip Granite tiles	7	05-May-26 08:00	13-May-26 10:00	05-May-26 08:00 A	12-May-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-T-PR-SL-AR-PO-30	Epoxy Paint	7	05-May-26 08:00	13-May-26 10:00	05-May-26 08:00 A	12-May-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-T-PR-SL-AR-PO-40	Cement Plaster	7	05-May-26 08:00	13-May-26 10:00	05-May-26 08:00 A	12-May-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-T-PR-SL-AR-PO-50	Acrylic Paint	7	05-May-26 08:00	13-May-26 10:00	05-May-26 08:00 A	12-May-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-T-PR-SL-AR-PO-60	Stone Cladding	7	05-May-26 08:00	13-May-26 10:00	05-May-26 08:00 A	12-May-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-T-PR-SL-AR-PO-70	Phenolic Partition	7	05-May-26 08:00	13-May-26 10:00	05-May-26 08:00 A	12-May-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-T-PR-SL-AR-PO-80	Glass Partition	7	05-May-26 08:00	13-May-26 10:00	05-May-26 08:00 A	12-May-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-T-PR-SL-AR-PO-90	Gypsum Boards	7	05-May-26 08:00	13-May-26 10:00	05-May-26 08:00 A	12-May-26 17:00 A	0.00	0.00	0.00	100%	100%	0
METAL WORK		7	05-May-26 08:00	13-May-26 10:00	05-May-26 08:00 A	12-May-26 17:00 A	0.00	0.00	0.00	0%	0%	0
PG-T-PR-SL-MT-PO-10	Galvanized Steel Ladder	7	05-May-26 08:00	13-May-26 10:00	05-May-26 08:00 A	12-May-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-T-PR-SL-MT-PO-20	Galvanized Steel Roof Scupper	7	05-May-26 08:00	13-May-26 10:00	05-May-26 08:00 A	12-May-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-T-PR-SL-MT-PO-30	Galvanized Steel Cover with frame	7	05-May-26 08:00	13-May-26 10:00	05-May-26 08:00 A	12-May-26 17:00 A	0.00	0.00	0.00	100%	100%	0
HVAC WORK		7	05-May-26 08:00	13-May-26 10:00	05-May-26 08:00 A	12-May-26 17:00 A	0.00	0.00	0.00	0%	0%	0
PG-T-PR-SL-AC-PO-10	Split Air Conditioning Unit	7	05-May-26 08:00	13-May-26 10:00	05-May-26 08:00 A	12-May-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-T-PR-SL-AC-PO-20	Air Duct	7	05-May-26 08:00	13-May-26 10:00	05-May-26 08:00 A	12-May-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-T-PR-SL-AC-PO-30	Diffusers and Grills	7	05-May-26 08:00	13-May-26 10:00	05-May-26 08:00 A	12-May-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-T-PR-SL-AC-PO-40	Exhaust fans	7	05-May-26 08:00	13-May-26 10:00	05-May-26 08:00 A	12-May-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PLUMBING WORK		7	05-May-26 08:00	13-May-26 10:00	05-May-26 08:00 A	12-May-26 17:00 A	0.00	0.00	0.00	0%	0%	0
PG-T-PR-SL-PB-PO-10	PPR Pipes & Valves	7	05-May-26 08:00	13-May-26 10:00	05-May-26 08:00 A	12-May-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-T-PR-SL-PB-PO-20	UPCV Pipes	7	05-May-26 08:00	13-May-26 10:00	05-May-26 08:00 A	12-May-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-T-PR-SL-PB-PO-30	Sanitary Drainage Fixtures	7	05-May-26 08:00	13-May-26 10:00	05-May-26 08:00 A	12-May-26 17:00 A	0.00	0.00	0.00	100%	100%	0
IRRIGATION WORK		7	05-May-26 08:00	13-May-26 10:00	05-May-26 08:00 A	12-May-26 17:00 A	0.00	0.00	0.00	0%	0%	0
PG-T-PR-SL-IR-PO-10	Gate Valve including valve box	7	05-May-26 08:00	13-May-26 10:00	05-May-26 08:00 A	12-May-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-T-PR-SL-IR-PO-20	Bubblers and Spreyers	7	05-May-26 08:00	13-May-26 10:00	05-May-26 08:00 A	12-May-26 17:00 A	0.00	0.00	0.00	100%	100%	0
ELECTRICAL WORK		97	11-May-26 08:00	02-Jul-26 17:00	11-May-26 08:00 A	27-Aug-26 17:00 A	0.00	0.00	0.00	0%	0%	-48
PG-T-PR-SL-EL-PO-10	Wiring Devices Materials(Completed)	35	11-May-26 08:00	25-Jun-26 10:00	11-May-26 08:00 A	24-Jun-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-T-PR-SL-EL-PO-10_R	Wiring Devices Materials(Remaining)	7	25-Jun-26 08:00	02-Jul-26 17:00	20-Aug-26 08:00 A	27-Aug-26 17:00 A	0.00	0.00	0.00	100%	100%	0
FIRE FIGHTING WORK		94	11-May-26 08:00	29-Jun-26 17:00	11-May-26 08:00 A	27-Aug-26 17:00 A	0.00	0.00	0.00	0%	0%	-51
PG-T-PR-SL-FF-PO-10	Fire Extinguishers(Completed)	35	11-May-26 08:00	25-Jun-26 10:00	11-May-26 08:00 A	24-Jun-26 17:00 A	0.00	0.00	0.00	100%	100%	0
PG-T-PR-SL-FF-PO-10_R	Fire Extinguishers(Remaining)	4	25-Jun-26 08:00	29-Jun-26 17:00	20-Aug-26 08:00 A	27-Aug-26 17:00 A	0.00	0.00	0.00	100%	100%	-3
DELIVERY TO SITE		188	01-Mar-26 08:00	22-Jul-26 17:00	01-Mar-26 08:00 A	25-Oct-26 09:36	504,666.45	500,998.54	504,666.45	100%	99.27%	-79
EXTERNAL / LANDSCAPE WORK		171	01-Mar-26 08:00	22-Jul-26 17:00	01-Mar-26 08:00 A	24-Oct-26 17:00	346,880.61	344,882.80	346,880.61	100%	99.42%	-79
PG-T-PR-SL-LS-DL-10	Backfilling Materials	43	01-Mar-26 08:00	23-Apr-26 17:00	01-Mar-26 08:00 A	24-Apr-26 17:00 A	91,125.00	91,125.00	91,125.00	100%	100%	0
PG-T-PR-SL-LS-DL-20	Interlock tiles	13	29-Apr-26 08:00	13-May-26 17:00	29-Apr-26 08:00 A	13-May-26 17:00 A	96,438.60	96,438.60	96,438.60	100%	100%	0
PG-T-PR-SL-LS-DL-30	Compacted Natural Ground Soil	41	03-Mar-26 08:00	23-Apr-26 17:00	03-Mar-26 08:00 A	24-Apr-26 17:00 A	11,583.00	11,583.00	11,583.00	100%	100%	0
PG-T-PR-SL-LS-DL-40	Curb Stone	13	29-Apr-26 08:00	13-May-26 17:00	29-Apr-26 08:00 A	13-May-26 17:00 A	93,058.20	93,058.20	93,058.20	100%	100%	0
PG-T-PR-SL-LS-DL-50	Thermoplastic pavement road marking	1	13-May-26 08:00	13-May-26 17:00	13-May-26 08:00 A	13-May-26 17:00 A	4,730.67	4,730.67	4,730.67	100%	100%	0
PG-T-PR-SL-LS-DL-60	Traffic Signages(Completed)	33	13-May-26 08:00	24-Jun-26 17:00	13-May-26 08:00 A	24-Jun-26 17:00 A	1,071.14	1,071.14	1,071.14	100%	100%	0
PG-T-PR-SL-LS-DL-60_R	Traffic Signages(Remaining)	10	12-Jul-26 08:00	22-Jul-26 17:00	27-Aug-26 08:00 A	24-Oct-26 17:00	714.10	642.69	714.10	100%	90%	-39
PG-T-PR-SL-LS-DL-70	Trees(Completed)	33	13-May-26 08:00	24-Jun-26 17:00	13-May-26 08:00 A	24-Jun-26 17:00 A	12,452.94	12,452.94	12,452.94	100%	100%	0
PG-T-PR-SL-LS-DL-70_R	Trees(Remaining)	10	12-Jul-26 08:00	22-Jul-26 17:00	27-Aug-26 08:00 A	24-Oct-26 17:00	8,301.96	7,471.76	8,301.96	100%	90%	-39
PG-T-PR-SL-LS-DL-80	Lawn(Completed)	33	13-May-26 08:00	24-Jun-26 17:00	13-May-26 08:00 A	24-Jun-26 17:00 A	16,443.00	16,443.00	16,443.00	100%	100%	0
PG-T-PR-SL-LS-DL-80_R	Lawn(Remaining)	10	12-Jul-26 08:00	22-Jul-26 17:00	27-Aug-26 08:00 A	24-Oct-26 17:00	10,962.00	9,865.80	10,962.00	100%	90%	-39
CONCRETE WORK		52	10-Mar-26 08:00	13-May-26 17:00	10-Mar-26 08:00 A	13-May-26 17:00 A	14,485.23	14,485.23	14,485.23	100%	100%	0
PG-T-PR-SL-CO-DL-10	Steel Rebar	18	23-Apr-26 08:00	13-May-26 17:00	23-Apr-26 08:00 A	13-May-26 17:00 A	4,291.38	4,291.38	4,291.38	100%	100%	0
PG-T-PR-SL-CO-DL-20	Concrete	35	10-Mar-26 08:00	23-Apr-26 17:00	10-Mar-26 08:00 A	24-Apr-26 17:00 A	4,669.65	4,669.65	4,669.65	100%	100%	0
PG-T-PR-SL-CO-DL-30	Screed	18	23-Apr-26 08:00	13-May-26 17:00	23-Apr-26 08:00 A	13-May-26 17:00 A	1,058.40	1,058.40	1,058.40	100%	100%	0

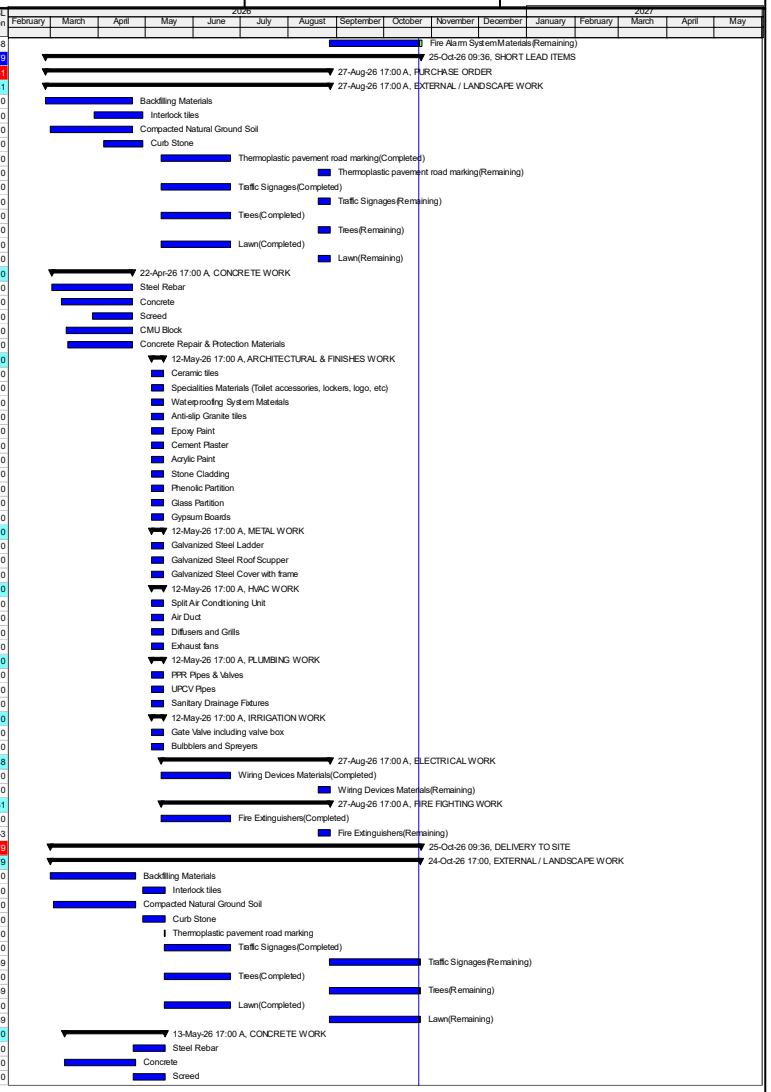

Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining W...
Milestone
summary

Baseline Schedule Rev.00

PLAYGROUNDS INITIATIVE - QASSIM, HAIL & TABUK - 25-Oct-2026

Activity ID	Activity Name	O.D	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Schedule % Complete	Performance % Complete	Variance - BL Project Duration
PG-T-PR-SL-CO-DL-40	CMU Block	18	23-Apr-26 08:00	13-May-26 17:00	23-Apr-26 08:00 A	13-May-26 17:00 A	1,117.80	1,117.80	1,117.80	100%	100%	0
PG-T-PR-SL-CO-DL-50	Concrete Repair & Protection Materials	18	23-Apr-26 08:00	13-May-26 17:00	23-Apr-26 08:00 A	13-May-26 17:00 A	3,348.00	3,348.00	3,348.00	100%	100%	0
ARCHITECTURAL & FINISHES WORK		7	06-May-26 08:00	13-May-26 17:00	06-May-26 08:00 A	13-May-26 17:00 A	71,383.95	71,383.95	71,383.95	100%	100%	0
PG-T-PR-SL-AR-DL-10	Ceramic tiles	7	06-May-26 08:00	13-May-26 17:00	06-May-26 08:00 A	13-May-26 17:00 A	5,147.55	5,147.55	5,147.55	100%	100%	0
PG-T-PR-SL-AR-DL-100	Specialities Materials (Toilet accessories, lockers, logo, etc)	7	06-May-26 08:00	13-May-26 17:00	06-May-26 08:00 A	13-May-26 17:00 A	20,365.83	20,365.83	20,365.83	100%	100%	0
PG-T-PR-SL-AR-DL-110	Waterproofing System Materials	7	06-May-26 08:00	13-May-26 17:00	06-May-26 08:00 A	13-May-26 17:00 A	4,897.80	4,897.80	4,897.80	100%	100%	0
PG-T-PR-SL-AR-DL-20	Anti-slip Granite tiles	7	06-May-26 08:00	13-May-26 17:00	06-May-26 08:00 A	13-May-26 17:00 A	4,819.50	4,819.50	4,819.50	100%	100%	0
PG-T-PR-SL-AR-DL-30	Epoxy Paint	7	06-May-26 08:00	13-May-26 17:00	06-May-26 08:00 A	13-May-26 17:00 A	1,000.62	1,000.62	1,000.62	100%	100%	0
PG-T-PR-SL-AR-DL-40	Cement Plaster	7	06-May-26 08:00	13-May-26 17:00	06-May-26 08:00 A	13-May-26 17:00 A	1,992.33	1,992.33	1,992.33	100%	100%	0
PG-T-PR-SL-AR-DL-50	Acrylic Paint	7	06-May-26 08:00	13-May-26 17:00	06-May-26 08:00 A	13-May-26 17:00 A	1,331.10	1,331.10	1,331.10	100%	100%	0
PG-T-PR-SL-AR-DL-60	Stone Cladding	7	06-May-26 08:00	13-May-26 17:00	06-May-26 08:00 A	13-May-26 17:00 A	16,669.80	16,669.80	16,669.80	100%	100%	0
PG-T-PR-SL-AR-DL-70	Phenolic Partition	7	06-May-26 08:00	13-May-26 17:00	06-May-26 08:00 A	13-May-26 17:00 A	12,063.60	12,063.60	12,063.60	100%	100%	0
PG-T-PR-SL-AR-DL-80	Glass Partition	7	06-May-26 08:00	13-May-26 17:00	06-May-26 08:00 A	13-May-26 17:00 A	1,398.60	1,398.60	1,398.60	100%	100%	0
PG-T-PR-SL-AR-DL-90	Gypsum Boards	7	06-May-26 08:00	13-May-26 17:00	06-May-26 08:00 A	13-May-26 17:00 A	1,697.22	1,697.22	1,697.22	100%	100%	0
METAL WORK		135	06-May-26 08:00	08-Jul-26 17:00	06-May-26 08:00 A	25-Oct-26 09:36	4,310.01	4,137.61	4,310.01	100%	96%	-91
PG-T-PR-SL-MT-DL-10	Galvanized Steel Ladder(Completed)	39	06-May-26 08:00	24-Jun-26 17:00	06-May-26 08:00 A	24-Jun-26 17:00 A	1,954.04	1,954.04	1,954.04	100%	100%	0
PG-T-PR-SL-MT-DL-10_R	Galvanized Steel Ladder(Remaining)	12	25-Jun-26 08:00	08-Jul-26 17:00	23-Sep-26 08:00 A	25-Oct-26 09:36	1,302.70	1,172.43	1,302.70	100%	90%	-14
PG-T-PR-SL-MT-DL-20	Galvanized Steel Roof Scupper(Completed)	39	06-May-26 08:00	24-Jun-26 17:00	06-May-26 08:00 A	24-Jun-26 17:00 A	169.13	169.13	169.13	100%	100%	0
PG-T-PR-SL-MT-DL-20_R	Galvanized Steel Roof Scupper(Remaining)	12	25-Jun-26 08:00	08-Jul-26 17:00	24-Sep-26 08:00 A	25-Oct-26 09:36	112.75	101.48	112.75	100%	90%	-14
PG-T-PR-SL-MT-DL-30	Galvanized Steel Cover with frame(Completed)	39	06-May-26 08:00	24-Jun-26 17:00	06-May-26 08:00 A	24-Jun-26 17:00 A	462.83	462.83	462.83	100%	100%	0
PG-T-PR-SL-MT-DL-30_R	Galvanized Steel Cover with frame(Remaining)	12	25-Jun-26 08:00	08-Jul-26 17:00	24-Sep-26 08:00 A	25-Oct-26 09:36	308.56	277.70	308.56	100%	90%	-14
HVAC WORK		7	06-May-26 08:00	13-May-26 17:00	06-May-26 08:00 A	13-May-26 17:00 A	5,457.24	5,457.24	5,457.24	100%	100%	0
PG-T-PR-SL-AC-DL-10	Split Air Conditioning Unit	7	06-May-26 08:00	13-May-26 17:00	06-May-26 08:00 A	13-May-26 17:00 A	2,789.37	2,789.37	2,789.37	100%	100%	0
PG-T-PR-SL-AC-DL-20	Air Duct	7	06-May-26 08:00	13-May-26 17:00	06-May-26 08:00 A	13-May-26 17:00 A	1,404.00	1,404.00	1,404.00	100%	100%	0
PG-T-PR-SL-AC-DL-30	Diffusers and Grills	7	06-May-26 08:00	13-May-26 17:00	06-May-26 08:00 A	13-May-26 17:00 A	668.79	668.79	668.79	100%	100%	0
PG-T-PR-SL-AC-DL-40	Exhaust fans	7	06-May-26 08:00	13-May-26 17:00	06-May-26 08:00 A	13-May-26 17:00 A	595.08	595.08	595.08	100%	100%	0
PLUMBING WORK		7	06-May-26 08:00	13-May-26 17:00	06-May-26 08:00 A	13-May-26 17:00 A	28,323.27	28,323.27	28,323.27	100%	100%	0
PG-T-PR-SL-PB-DL-10	PPR Pipes & Valves	7	06-May-26 08:00	13-May-26 17:00	06-May-26 08:00 A	13-May-26 17:00 A	2,386.80	2,386.80	2,386.80	100%	100%	0
PG-T-PR-SL-PB-DL-20	UPCV Pipes	7	06-May-26 08:00	13-May-26 17:00	06-May-26 08:00 A	13-May-26 17:00 A	3,016.71	3,016.71	3,016.71	100%	100%	0
PG-T-PR-SL-PB-DL-30	Sanitary Drainage Fixtures	7	06-May-26 08:00	13-May-26 17:00	06-May-26 08:00 A	13-May-26 17:00 A	22,919.76	22,919.76	22,919.76	100%	100%	0
IRRIGATION WORK		97	06-May-26 08:00	05-Jul-26 17:00	06-May-26 08:00 A	24-Oct-26 15:48	29,954.07	28,456.37	29,954.07	100%	95%	-94
PG-T-PR-SL-IR-DL-10	Gate Valve including valve box(Completed)	39	06-May-26 08:00	24-Jun-26 17:00	06-May-26 08:00 A	24-Jun-26 17:00 A	1,859.76	1,859.76	1,859.76	100%	100%	0
PG-T-PR-SL-IR-DL-10_R	Gate Valve including valve box(Remaining)	9	25-Jun-26 08:00	05-Jul-26 17:00	07-Aug-26 08:00 A	24-Oct-26 15:48	1,859.76	1,673.78	1,859.76	100%	90%	-57
PG-T-PR-SL-IR-DL-20	Bubblers and Spreyers(Completed)	39	06-May-26 08:00	24-Jun-26 17:00	06-May-26 08:00 A	24-Jun-26 17:00 A	13,117.28	13,117.28	13,117.28	100%	100%	0
PG-T-PR-SL-IR-DL-20_R	Bubblers and Spreyers(Remaining)	9	25-Jun-26 08:00	05-Jul-26 17:00	20-Aug-26 08:00 A	24-Oct-26 15:48	13,117.28	11,805.55	13,117.28	100%	90%	-46
ELECTRICAL WORK		118	13-May-26 08:00	16-Jul-26 17:00	13-May-26 08:00 A	15-Oct-26 17:00 A	3,667.68	3,667.68	3,667.68	100%	100%	-77
PG-T-PR-SL-EL-DL-10	Wiring Devices Materials(Completed)	33	13-May-26 08:00	24-Jun-26 17:00	13-May-26 08:00 A	24-Jun-26 17:00 A	1,467.07	1,467.07	1,467.07	100%	100%	0
PG-T-PR-SL-EL-DL-10_R	Wiring Devices Materials(Remaining)	12	04-Jul-26 08:00	16-Jul-26 17:00	19-Sep-26 08:00 A	15-Oct-26 17:00 A	2,200.61	2,200.61	2,200.61	100%	100%	-11
FIRE FIGHTING WORK		126	13-May-26 08:00	09-Jul-26 17:00	13-May-26 08:00 A	15-Oct-26 17:00 A	204.39	204.39	204.39	100%	100%	-83
PG-T-PR-SL-FF-DL-10	Fire Extinguishers(Completed)	33	13-May-26 08:00	24-Jun-26 17:00	13-May-26 08:00 A	24-Jun-26 17:00 A	81.76	81.76	81.76	100%	100%	0
PG-T-PR-SL-FF-DL-10_R	Fire Extinguishers(Remaining)	9	30-Jun-26 08:00	09-Jul-26 17:00	27-Sep-26 08:00 A	15-Oct-26 17:00 A	122.63	122.63	122.63	100%	100%	-8
CONSTRUCTION STAGE		263	24-Mar-26 08:00	14-Dec-26 17:00	24-Mar-26 08:00 A	30-Jan-27 17:00	5,438,906.71	3,588,645.67	6,814,680.60	79.81%	52.66%	-40
PLAYGROUND AND LANDSCAPING WORKS		246	24-Mar-26 08:00	14-Dec-26 17:00	24-Mar-26 08:00 A	10-Jan-27 16:12	2,013,546.81	2,072,784.96	2,311,795.02	87.1%	89.66%	-23
CUT AND FILL		38	24-Mar-26 08:00	06-May-26 17:00	24-Mar-26 08:00 A	06-May-26 17:00 A	228,240.00	228,240.00	228,240.00	100%	100%	0
PG-T-CON-EXCF-10	Existing Soil Excavation Works	22	24-Mar-26 08:00	18-Apr-26 17:00	24-Mar-26 08:00 A	18-Apr-26 17:00 A	64,800.00	64,800.00	64,800.00	100%	100%	0
PG-T-CON-EXCF-20	Soil Replacement Works	18	07-Apr-26 08:00	27-Apr-26 17:00	07-Apr-26 08:00 A	27-Apr-26 17:00 A	25,740.00	25,740.00	25,740.00	100%	100%	0
PG-T-CON-EXCF-30	Levelling & Backfilling Works	17	18-Apr-26 08:00	06-May-26 17:00	18-Apr-26 08:00 A	06-May-26 17:00 A	137,700.00	137,700.00	137,700.00	100%	100%	0
PLAYGROUND WORKS		186	23-Apr-26 08:00	07-Dec-26 17:00	23-Apr-26 08:00 A	03-Dec-26 15:00	550,592.94	537,405.24	623,491.20	88.31%	86.19%	3
FOOTBALL PLAYGROUND WORKS		170	23-Apr-26 08:00	17-Nov-26 17:00	23-Apr-26 08:00 A	12-Nov-26 16:12	307,563.00	297,308.33	333,290.16	92.28%	89.2%	4
PG-T-CON-EXFB-10	Subgrade Preparation and Compaction	12	23-Apr-26 08:00	06-May-26 17:00	23-Apr-26 08:00 A	06-May-26 17:00 A	23,667.00	23,667.00	23,667.00	100%	100%	0
PG-T-CON-EXFB-100	Markings and Signages	10	07-Nov-26 08:00	17-Nov-26 17:00	01-Nov-26 16:12	12-Nov-26 16:12	0.00	0.00	23,667.00	0%	0%	0
PG-T-CON-EXFB-110	Install Playground Benches	12	24-Oct-26 08:00	05-Nov-26 17:00	27-Aug-26 08:00 A	01-Nov-26 16:12	0.00	1,648.13	2,060.16	0%	80%	-44
PG-T-CON-EXFB-120	Installation of Lighting System	13	19-Aug-26 08:00	02-Sep-26 17:00	20-Aug-26 08:00 A	25-Oct-26 10:24	24,360.00	21,924.00	24,360.00	100%	90%	-42
PG-T-CON-EXFB-20	Sub-Base Laying and Compaction	8	28-Apr-26 08:00	06-May-26 17:00	28-Apr-26 08:00 A	06-May-26 17:00 A	23,667.00	23,667.00	23,667.00	100%	100%	0
PG-T-CON-EXFB-30	Base Course Laying and Compaction	33	06-May-26 08:00	17-Jun-26 17:00	06-May-26 08:00 A	17-Jun-26 17:00 A	23,667.00	23,667.00	23,667.00	100%	100%	0
PG-T-CON-EXFB-40	Tartan flooring	15	17-Sep-26 08:00	05-Oct-26 17:00	14-Aug-26 08:00 A	14-Aug-26 08:00 A	70,200.00	70,200.00	70,200.00	100%	100%	15
PG-T-CON-EXFB-50	Goal Post Foundation	17	30-Jul-26 08:00	18-Aug-26 17:00	23-Jul-26 08:00 A	14-Aug-26 17:00 A	35,500.50	35,500.50	35,500.50	100%	100%	-2
PG-T-CON-EXFB-60	Goal Post Installation & Alignment	15	06-Oct-26 08:00	22-Oct-26 17:00	20-Aug-26 08:00 A	29-Oct-26 12:00	35,500.50	28,400.40	35,500.50	100%	80%	-45
PG-T-CON-EXFB-70	Topsoil Placement(Completed)	33	13-May-26 08:00	24-Jun-26 17:00	13-May-26 08:00 A	24-Jun-26 17:00 A	9,466.80	9,466.80	9,466.80	100%	100%	0
PG-T-CON-EXFB-70_R	Topsoil Placement(Remaining)	15	13-Jul-26 08:00	29-Jul-26 17:00	09-Jul-26 08:00 A	12-Jul-26 17:00 A	14,200.20	14,200.20	14,200.20	100%	100%	12
PG-T-CON-EXFB-80	Fine Grading & Leveling	15	25-Jun-26 08:00	12-Jul-26 17:00	07-Jul-26 08:00 A	12-Jul-26 17:00 A	23,667.00	23,667.00	23,667.00	100%	100%	10
PG-T-CON-EXFB-90	Turfing / Seeding Works	12	03-Sep-26 08:00	16-Sep-26 17:00	14-Aug-26 08:00 A	26-Oct-26 12:00	23,667.00	21,300.30	23,667.00	100%	90%	-50
BASKETBALL PLAYGROUND WORKS		163	06-May-26 08:00	17-Nov-26 17:00	06-May-26 08:00 A	19-Nov-26 09:36	167,045.38	157,108.46	173,211.12	96.44%	90.7%	-1
PG-T-CON-EXBB-10	Subgrade Preparation and Compaction	1	06-May-26 08:00	06-May-26 17:00	06-May-26 08:00 A	06-May-26 17:00 A	15,472.08	15,472.08	15,472.08	100%	100%	0
PG-T-CON-EXBB-100	Install Playground Benches	16	31-Oct-26 08:00	17-Nov-26 17:00	27-Aug-26 08:00 A	19-Nov-26 09:36	0.00	1,390.61	1,545.12	0%	90%	-55
PG-T-CON-EXBB-20	Sub-Base Laying and Compaction	1	06-May-26 08:00	06-May-26 17:00	06-May-26 08:00 A	06-May-26 17:00 A	15,472.08	15,472.08	15,472.08	100%	100%	0
PG-T-CON-EXBB-30	Base Course Laying and Compaction	33	06-May-26 08:00	17-Jun-26 17:00	06-May-26 08:00 A	17-Jun-26 17:00 A	15,472.08	15,472.08	15,472.08	100%	100%	0
PG-T-CON-EXBB-40	Tartan flooring	17	11-Aug-26 08:00	30-Aug-26 17:00	12-Jul-26 08:00 A	14-Aug-26 17:00 A	52,650.00	52,650.00	52,650.00	100%	100%	-12
PG-T-CON-EXBB-50	Basketball Pole Foundation	25	25-Jun-26 08:00	23-Jul-26 17:00	06-Aug-26 08:00 A	14-Aug-26 17:00 A	15,472.08	15,472.08	15,472.08	100%	100%	18
PG-T-CON-EXBB-60	Basketball Pole Installation & Alignment	18	19-Sep-26 08:00	10-Oct-26 17:00	20-Aug-26 08:00 A	28-Oct-26 12:48	15,472.08	13,924.87	15,472.08	100%	90%	-41
PG-T-CON-EXBB-70	Floor Surface Curing(Completed)	7	17-Jun-26 08:00	24-Jun-26 17:00	17-Jun-26 08:00 A	24-Jun-26 17:00 A	7,736.04	7,736.04	7,736.04	100%	100%	0
PG-T-CON-EXBB-70_R	Floor Surface Curing(Remaining)	15	25-Jul-26 08:00	10-Aug-26 17:00	09-Jul-26 08:00 A	12-Jul-26 17:00 A	7,736.04	7,736.04	7,736.04	100%	100%	12
PG-T-CON-EXBB-80	Court Line Marking	16	31-Aug-26 08:00	17-Sep-26 17:00	20-Aug-26 08:00 A	26-Oct-26 15:24	13,091.76	11,782.58	13,091.76	100%	90%	-41




Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining W...
Milestone
summary

Baseline Schedule Rev.00

PLAYGROUNDS INITIATIVE - QASSIM, HAIL & TABUK - 25-Oct-2026

Activity ID	Activity Name	O.D	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Schedule % Complete	Performance % Complete	Variance - BL Project Duration
PG-T-CON-EXBB-90	Backboard & Hoop Installation	17	11-Oct-26 08:00	29-Oct-26 17:00	28-Oct-26 12:48	17-Nov-26 12:48	8,471.14	0.00	13,091.76	64.71%	0%	0
PADEL PLAYGROUND WORKS		175	06-May-26 08:00	07-Dec-26 17:00	06-May-26 08:00 A	03-Dec-26 15:00	75,984.56	82,988.45	116,989.92	64.95%	70.94%	3
PG-T-CON-EXPD-10	Excavation For Fence Footing(Completed)	39	06-May-26 08:00	24-Jun-26 17:00	06-May-26 08:00 A	24-Jun-26 17:00 A	16,243.20	16,243.20	16,243.20	100%	100%	0
PG-T-CON-EXPD-10_R	Excavation For Fence Footing(Remaining)	8	25-Jun-26 08:00	04-Jul-26 17:00	06-Aug-26 08:00 A	14-Aug-26 17:00 A	1,804.80	1,804.80	1,804.80	100%	100%	1
PG-T-CON-EXPD-20	RC Foundations For Fence(Completed)	13	10-Jun-26 08:00	24-Jun-26 17:00	10-Jun-26 08:00 A	24-Jun-26 17:00 A	1,767.48	1,767.48	1,767.48	100%	100%	0
PG-T-CON-EXPD-20_R	RC Foundations For Fence(Remaining)	20	05-Jul-26 08:00	27-Jul-26 17:00	14-Aug-26 08:00 A	27-Aug-26 17:00 A	1,767.48	1,767.48	1,767.48	100%	100%	8
PG-T-CON-EXPD-30	Tartan Flooring Layers(Completed)	7	17-Jun-26 08:00	24-Jun-26 17:00	17-Jun-26 08:00 A	24-Jun-26 17:00 A	26,325.00	26,325.00	26,325.00	100%	100%	0
PG-T-CON-EXPD-30_R	Tartan Flooring Layers(Remaining)	17	13-Oct-26 08:00	01-Nov-26 17:00	20-Aug-26 08:00 A	12-Nov-26 12:00	13,936.76	23,692.50	26,325.00	52.94%	90%	-55
PG-T-CON-EXPD-40	Steel Structure & Fence Supports Installation	20	08-Aug-26 08:00	30-Aug-26 17:00	20-Aug-26 08:00 A	27-Oct-26 09:36	3,534.96	3,181.46	3,534.96	100%	90%	-37
PG-T-CON-EXPD-50	Tempered Glass Installation	18	21-Sep-26 08:00	12-Oct-26 17:00	20-Oct-26 08:00 A	10-Nov-26 15:24	5,302.44	2,120.98	5,302.44	100%	40%	-1
PG-T-CON-EXPD-60	Chain Link Fence & Gates Installation	18	31-Aug-26 08:00	20-Sep-26 17:00	20-Aug-26 08:00 A	28-Oct-26 17:00	5,302.44	4,772.20	5,302.44	100%	90%	-41
PG-T-CON-EXPD-70	Court Accessories Installation	16	02-Nov-26 08:00	19-Nov-26 17:00	12-Nov-26 12:00	01-Dec-26 12:00	0.00	0.00	27,072.00	0%	0%	0
PG-T-CON-EXPD-80	Install Playground Benches	15	21-Nov-26 08:00	07-Dec-26 17:00	27-Aug-26 08:00 A	03-Dec-26 15:00	0.00	1,313.35	1,545.12	0%	85%	-69
GENERAL SITE WORKS		226	16-Apr-26 08:00	14-Dec-26 17:00	16-Apr-26 08:00 A	10-Jan-27 16:12	594,275.82	536,348.31	656,604.42	90.51%	81.69%	-23
FENCE WORKS		160	16-Apr-26 08:00	17-Aug-26 17:00	16-Apr-26 08:00 A	15-Oct-26 17:00 A	32,909.40	32,909.40	32,909.40	100%	100%	-50
PG-T-CON-EXGN-FN-10	Excavation for fence foundation	3	16-Apr-26 08:00	19-Apr-26 17:00	16-Apr-26 08:00 A	19-Apr-26 17:00 A	6,581.88	6,581.88	6,581.88	100%	100%	0
PG-T-CON-EXGN-FN-20	Concrete Foundations for Fence	12	13-Jul-26 08:00	26-Jul-26 17:00	13-Aug-26 08:00 A	14-Oct-26 17:00 A	6,581.88	6,581.88	6,581.88	100%	100%	-41
PG-T-CON-EXGN-FN-30	Installation of Galvanized Steel Posts & Framing	7	27-Jul-26 08:00	03-Aug-26 17:00	20-Aug-26 08:00 A	15-Oct-26 17:00 A	6,581.88	6,581.88	6,581.88	100%	100%	-41
PG-T-CON-EXGN-FN-40	Fixing of Chain Link Mesh, Tensioning & Bracing	6	04-Aug-26 08:00	10-Aug-26 17:00	20-Sep-26 08:24 A	15-Oct-26 17:00 A	6,581.88	6,581.88	6,581.88	100%	100%	-16
PG-T-CON-EXGN-FN-50	Installation of Gates	6	11-Aug-26 08:00	17-Aug-26 17:00	11-Oct-26 08:00 A	15-Oct-26 17:00 A	6,581.88	6,581.88	6,581.88	100%	100%	1
MECHANICAL WORK		154	12-May-26 08:00	10-Aug-26 17:00	12-May-26 08:00 A	14-Nov-26 10:24	230,187.54	201,030.97	230,187.54	100%	87.33%	-80
STORM WATER AND UTILITY WORK		149	12-May-26 08:00	04-Aug-26 17:00	12-May-26 08:00 A	08-Nov-26 10:24	27,252.00	16,806.00	27,252.00	100%	61.67%	-80
PG-T-CON-EXGN-M-10	Excavation	2	12-May-26 08:00	13-May-26 17:00	12-May-26 08:00 A	13-May-26 17:00 A	3,096.00	3,096.00	3,096.00	100%	100%	0
PG-T-CON-EXGN-M-20	Bedding preparation & level control(Completed)	13	10-Jun-26 08:00	24-Jun-26 17:00	10-Jun-26 08:00 A	24-Jun-26 17:00 A	1,548.00	1,548.00	1,548.00	100%	100%	0
PG-T-CON-EXGN-M-20_R	Bedding preparation & level control(Remaining)	5	25-Jun-26 08:00	30-Jun-26 17:00	12-Jul-26 08:00 A	27-Aug-26 17:00 A	516.00	516.00	516.00	100%	100%	-36
PG-T-CON-EXGN-M-30	Manhole Installation	5	01-Jul-26 08:00	06-Jul-26 17:00	20-Aug-26 08:00 A	24-Oct-26 17:00	5,160.00	4,128.00	5,160.00	100%	80%	-50
PG-T-CON-EXGN-M-40	150 mm uPVC pipe laying & jointing	4	07-Jul-26 08:00	11-Jul-26 17:00	20-Sep-26 10:00 A	26-Oct-26 09:36	10,740.00	7,518.00	10,740.00	100%	70%	-26
PG-T-CON-EXGN-M-50	Concrete Encasement	3	12-Jul-26 08:00	14-Jul-26 17:00	26-Oct-26 09:36	29-Oct-26 09:36	2,064.00	0.00	2,064.00	100%	0%	0
PG-T-CON-EXGN-M-60	Backfilling & Compaction	3	15-Jul-26 08:00	18-Jul-26 17:00	29-Oct-26 09:36	02-Nov-26 09:36	2,064.00	0.00	2,064.00	100%	0%	0
PG-T-CON-EXGN-M-70	Surface Reinstatement & Civil Works	4	01-Aug-26 08:00	04-Aug-26 17:00	03-Nov-26 10:24	08-Nov-26 10:24	2,064.00	0.00	2,064.00	100%	0%	0
IRRIGATION SYSTEM WORKS		96	02-Jun-26 08:00	30-Jul-26 17:00	02-Jun-26 08:00 A	03-Nov-26 10:24	202,617.60	184,224.97	202,617.60	100%	90.92%	-80
PG-T-CON-EXGN-M-100	Installation of Bubblers and Sprinklers	5	26-Jul-26 08:00	30-Jul-26 17:00	20-Aug-26 08:00 A	03-Nov-26 10:24	58,299.00	52,469.10	58,299.00	100%	90%	-58
PG-T-CON-EXGN-M-80	Installation of HDPE Irrigation Pipe Network with Gate Valve and	20	02-Jun-26 08:00	24-Jun-26 17:00	02-Jun-26 08:00 A	24-Jun-26 17:00 A	18,691.26	18,691.26	18,691.26	100%	100%	0
PG-T-CON-EXGN-M-80_R	Installation of HDPE Irrigation Pipe Network with Gate Valve and	4	14-Jul-26 08:00	18-Jul-26 17:00	12-Jul-26 08:00 A	02-Nov-26 09:36	34,712.34	31,241.11	34,712.34	100%	90%	-92
PG-T-CON-EXGN-M-90	Installation of Irrigation Control System	6	19-Jul-26 08:00	25-Jul-26 17:00	20-Aug-26 08:00 A	02-Nov-26 15:24	90,915.00	81,823.50	90,915.00	100%	90%	-57
FIRE PROTECTION SYSTEM		5	05-Aug-26 08:00	10-Aug-26 17:00	08-Nov-26 10:24	14-Nov-26 10:24	317.94	0.00	317.94	100%	0%	0
PG-T-CON-EXGN-M-110	Fire Extinguisher Installation	5	05-Aug-26 08:00	10-Aug-26 17:00	08-Nov-26 10:24	14-Nov-26 10:24	317.94	0.00	317.94	100%	0%	0
ELECTRICAL WORK		180	08-Jun-26 08:00	07-Nov-26 17:00	08-Jun-26 08:00 A	20-Dec-26 16:12	324,720.48	272,439.15	345,859.68	93.89%	78.77%	-37
POWER, LIGHTING & GROUNDING		147	08-Jun-26 08:00	27-Sep-26 17:00	08-Jun-26 08:00 A	26-Nov-26 12:00	288,789.48	240,981.87	288,789.48	100%	83.45%	-52
PG-T-CON-EXGN-E-10	Excavation	3	08-Jun-26 08:00	10-Jun-26 17:00	08-Jun-26 08:00 A	10-Jun-26 17:00 A	69,621.12	69,621.12	69,621.12	100%	100%	0
PG-T-CON-EXGN-E-20	Foundation Work for Site Lighting Poles(Completed)	13	10-Jun-26 08:00	24-Jun-26 17:00	10-Jun-26 08:00 A	24-Jun-26 17:00 A	37,131.26	37,131.26	37,131.26	100%	100%	0
PG-T-CON-EXGN-E-20_R	Foundation Work for Site Lighting Poles(Remaining)	21	25-Jun-26 08:00	19-Jul-26 17:00	20-Aug-26 08:00 A	26-Oct-26 08:48	55,696.90	50,127.21	55,696.90	100%	90%	-35
PG-T-CON-EXGN-E-30	Lightning Protection System (LPS)	8	11-Aug-26 08:00	19-Aug-26 17:00	20-Aug-26 08:00 A	15-Nov-26 08:48	8,265.00	7,438.50	8,265.00	100%	90%	-65
PG-T-CON-EXGN-E-40	KWH Meter and MDB Installation	5	25-Aug-26 08:00	30-Aug-26 17:00	17-Sep-26 08:48 A	16-Nov-26 08:48	4,586.70	3,669.36	4,586.70	100%	80%	-45
PG-T-CON-EXGN-E-50	Power Panels and Distribution Boards	7	31-Aug-26 08:00	07-Sep-26 17:00	17-Sep-26 08:48 A	17-Nov-26 12:00	17,397.90	13,918.32	17,397.90	100%	80%	-44
PG-T-CON-EXGN-E-60	Site Lighting Poles Installation	6	08-Sep-26 08:00	14-Sep-26 17:00	17-Sep-26 08:48 A	18-Nov-26 14:36	69,621.12	55,696.90	69,621.12	100%	80%	-47
PG-T-CON-EXGN-E-70	Wiring Works	4	15-Sep-26 08:00	19-Sep-26 17:00	04-Oct-26 08:00 A	19-Nov-26 12:00	4,224.00	3,379.20	4,224.00	100%	80%	-37
PG-T-CON-EXGN-E-80	Lighting Fixtures with outlets Installation	6	20-Sep-26 08:00	27-Sep-26 17:00	19-Nov-26 12:00	26-Nov-26 12:00	22,245.48	0.00	22,245.48	100%	0%	0
ELV SYSTEMS (TELECOM, DATA, AV & CCTV)		25	28-Sep-26 08:00	26-Oct-26 17:00	22-Sep-26 08:48 A	08-Dec-26 12:00	28,266.00	25,887.60	43,146.00	65.51%	60%	-40
PG-T-CON-EXGN-E-100	Fiber Optic Pull Box Installation	3	01-Oct-26 08:00	04-Oct-26 17:00	22-Sep-26 08:48 A	29-Nov-26 16:12	619.80	371.88	619.80	100%	60%	-55
PG-T-CON-EXGN-E-110	Telephone and Data Outlet Installation	4	05-Oct-26 08:00	08-Oct-26 17:00	22-Sep-26 08:48 A	01-Dec-26 12:00	3,718.80	2,231.28	3,718.80	100%	60%	-55
PG-T-CON-EXGN-E-120	Telecom Equipment and AV HDMI Installation	4	10-Oct-26 08:00	13-Oct-26 17:00	22-Sep-26 08:48 A	03-Dec-26 08:48	15,249.12	9,149.47	15,249.12	100%	60%	-57
PG-T-CON-EXGN-E-130	CCTV Rack / Cabinet Installation	4	14-Oct-26 08:00	18-Oct-26 17:00	22-Sep-26 08:48 A	05-Dec-26 14:36	1,446.48	867.89	1,446.48	100%	60%	-59
PG-T-CON-EXGN-E-140	NVR and CCTV Monitor Installation	4	19-Oct-26 08:00	22-Oct-26 17:00	22-Sep-26 08:48 A	07-Dec-26 10:24	6,612.00	3,967.20	6,612.00	100%	60%	-60
PG-T-CON-EXGN-E-150	IP Camera Installation	3	24-Oct-26 08:00	26-Oct-26 17:00	22-Sep-26 08:48 A	08-Dec-26 12:00	0.00	8,928.00	14,880.00	0%	60%	-62
PG-T-CON-EXGN-E-90	ELV Containment & Cabling Works	3	28-Sep-26 08:00	30-Sep-26 17:00	22-Sep-26 08:48 A	28-Nov-26 14:36	619.80	371.88	619.80	100%	60%	-54
FIRE ALARM SYSTEM		32	01-Oct-26 08:00	07-Nov-26 17:00	13-Oct-26 08:00 A	20-Dec-26 16:12	7,665.00	5,569.68	13,924.20	55.05%	40%	-27
PG-T-CON-EXGN-E-160	Fire Alarm Containment & Cabling	8	01-Oct-26 08:00	10-Oct-26 17:00	13-Oct-26 08:00 A	03-Dec-26 12:00	1,983.60	793.44	1,983.60	100%	40%	-37
PG-T-CON-EXGN-E-170	Fire Alarm Control Panel (FACP) Installation	8	11-Oct-26 08:00	19-Oct-26 17:00	14-Oct-26 08:00 A	09-Dec-26 10:24	2,644.80	1,057.92	2,644.80	100%	40%	-40
PG-T-CON-EXGN-E-180	Initiating Devices (Detectors & Manual Pull Station)	8	20-Oct-26 08:00	28-Oct-26 17:00	15-Oct-26 08:00 A	15-Dec-26 08:48	3,036.60	3,239.04	8,097.60	37.5%	40%	-44
PG-T-CON-EXGN-E-190	Notification Appliances (Strobe with Sounder)	8	29-Oct-26 08:00	07-Nov-26 17:00	17-Oct-26 08:00 A	20-Dec-26 16:12	0.00	479.28	1,198.20	0%	40%	-48
PARKING WORK		161	17-Jun-26 08:00	11-Nov-26 17:00	17-Jun-26 08:00 A	20-Dec-26 16:12	5,788.80	25,728.00	40,207.80	14.4%	63.99%	-33
PG-T-CON-EXGN-PR-10	Installation of Parking Accessories	7	27-Oct-26 08:00	03-Nov-26 17:00	20-Aug-26 08:00 A	20-Oct-26 17:00 A	0.00	12,864.00	12,864.00	0%	100%	-45
PG-T-CON-EXGN-PR-20	Interlock tiles(Completed)	7	17-Jun-26 08:00	24-Jun-26 17:00	17-Jun-26 08:00 A	24-Jun-26 17:00 A	5,788.80	5,788.80	5,788.80	100%	100%	0
PG-T-CON-EXGN-PR-20_R	Interlock tiles(Remaining)	7	27-Oct-26 08:00	03-Nov-26 17:00	12-Jul-26 08:00 A	27-Aug-26 17:00 A	0.00	7,075.20	7,075.20	0%	100%	-34
PG-T-CON-EXGN-PR-30	Marking & Signages	7	04-Nov-26 08:00	11-Nov-26 17:00	12-Dec-26 16:12	20-Dec-26 16:12	0.00	0.00	14,479.80	0%	0%	0
SERVICE CONNECTION		183	10-Jun-26 08:00	14-Dec-26 17:00	10-Jun-26 08:00 A	10-Jan-27 16:12	669.60	4,240.80	7,440.00	9%	57%	-23
PG-T-CON-EXGN-S-C-10	Excavation & Trench Preparation(Completed)	13	10-Jun-26 08:00	24-Jun-26 17:00	10-Jun-26 08:00 A	24-Jun-26 17:00 A	669.60	669.60	669.60	100%	100%	0
PG-T-CON-EXGN-S-C-10_R	Excavation & Trench Preparation(Remaining)	7	04-Nov-26 08:00	11-Nov-26 17:00	12-Jul-26 08:00 A	23-Jul-26 17:00 A	0.00	1,562.40	1,562.40	0%	100%	-4
PG-T-CON-EXGN-S-C-20	HDPE Pipe Laying & Valve Installation	10	12-Nov-26 08:00	23-Nov-26 17:00	14-Aug-26 08:00 A	20-Dec-26 16:12	0.00	2,008.80	2,232.00	0%	90%	-99
PG-T-CON-EXGN-S-C-30	Connection to City Network	10	24-Nov-26 08:00	05-Dec-26 17:00	20-Dec-26 16:12	31-Dec-26 16:12	0.00	0.00	1,488.00	0%	0%	0
PG-T-CON-EXGN-S-C-40	Backfilling	8	06-Dec-26 08:00	14-Dec-26 17:00	31-Dec-26 16:12	10-Jan-27 16:12	0.00	0.00	1,488.00	0%	0%	0
LANDSCAPING WORKS		156	31-May-26 08:00	22-Nov-26 17:00	30-May-26 16:12 A	10-Nov-26 14:36	592,147.65	733,167.09	755,169.00	78.41%	97.09%	10

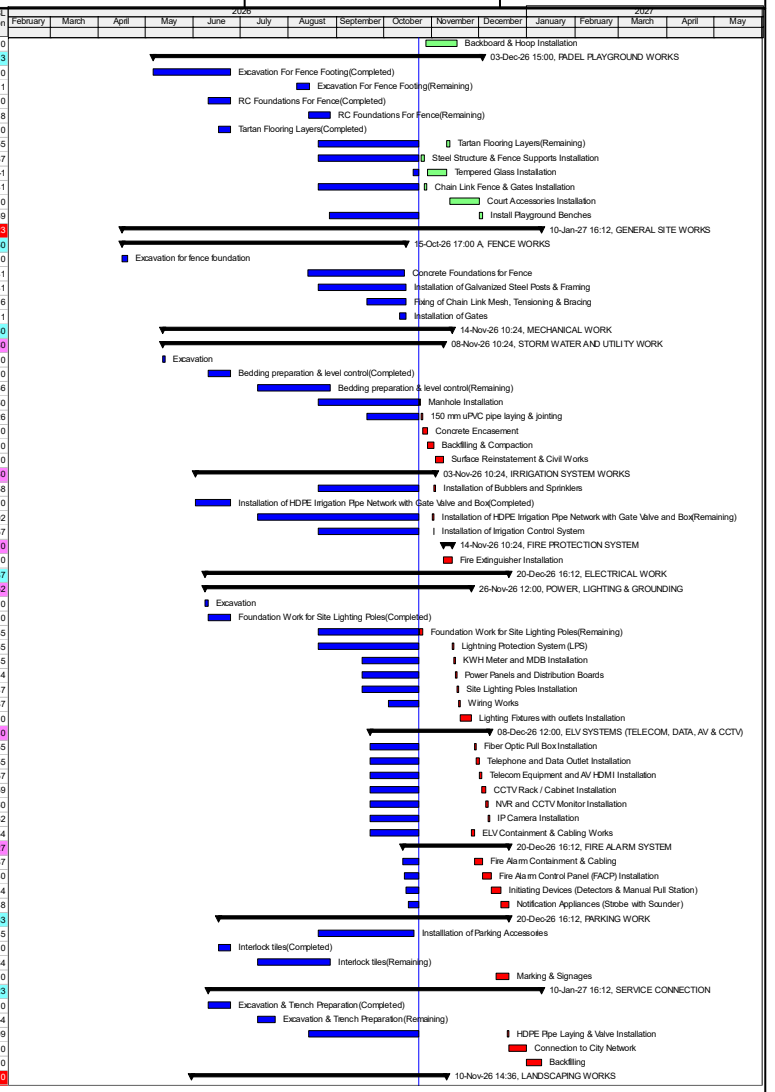


Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining W...
Milestone
summary

Baseline Schedule Rev.00

PLAYGROUNDS INITIATIVE - QASSIM, HAIL & TABUK - 25-Oct-2026

Activity ID	Activity Name	O.D	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Schedule % Complete	Performance % Complete	Variance - BL Project Duration
HARDSCAPE WORK		156	31-May-26 08:00	22-Nov-26 17:00	30-May-26 16:12 A	10-Nov-26 14:36	521,665.65	634,411.29	648,147.00	80.49%	97.88%	10
PG-T-CON-EXLS-HS-10	Curbstone Installation(Completed)	22	31-May-26 08:00	24-Jun-26 17:00	30-May-26 16:12 A	24-Jun-26 17:00 A	124,077.60	124,077.60	124,077.60	100%	100%	0
PG-T-CON-EXLS-HS-10_R	Curbstone Installation(Remaining)	8	17-Sep-26 08:00	27-Sep-26 17:00	12-Jul-26 08:00 A	27-Aug-26 17:00 A	82,718.40	82,718.40	82,718.40	100%	100%	-33
PG-T-CON-EXLS-HS-20	Interlock Tiles Grey Scale with Black Marble Chips(Completed)	22	31-May-26 08:00	24-Jun-26 17:00	30-May-26 16:12 A	24-Jun-26 17:00 A	40,656.00	40,656.00	40,656.00	100%	100%	0
PG-T-CON-EXLS-HS-20_R	Interlock Tiles Grey Scale with Black Marble Chips(Remaining)	10	28-Sep-26 08:00	08-Oct-26 17:00	27-Aug-26 08:00 A	04-Nov-26 12:00	60,984.00	54,885.60	60,984.00	100%	90%	-49
PG-T-CON-EXLS-HS-30	Stamped Concrete Floor(Completed)	13	10-Jun-26 08:00	24-Jun-26 17:00	10-Jun-26 08:00 A	24-Jun-26 17:00 A	43,470.00	43,470.00	43,470.00	100%	100%	0
PG-T-CON-EXLS-HS-30_R	Stamped Concrete Floor(Remaining)	10	10-Oct-26 08:00	20-Oct-26 17:00	30-Jul-26 08:00 A	21-Oct-26 17:00 A	43,470.00	43,470.00	43,470.00	100%	100%	-61
PG-T-CON-EXLS-HS-40	Bike Path and Walking Path Construction(Completed)	22	31-May-26 08:00	24-Jun-26 17:00	30-May-26 16:12 A	24-Jun-26 17:00 A	99,297.00	99,297.00	99,297.00	100%	100%	0
PG-T-CON-EXLS-HS-40_R	Bike Path and Walking Path Construction(Remaining)	8	21-Oct-26 08:00	29-Oct-26 17:00	23-Jul-26 08:00 A	27-Aug-26 17:00 A	20,310.75	81,243.00	81,243.00	25%	100%	-23
PG-T-CON-EXLS-HS-50	Install Recycled Precast Concrete Seats(Completed)	22	31-May-26 08:00	24-Jun-26 17:00	30-May-26 16:12 A	24-Jun-26 17:00 A	6,681.90	6,681.90	6,681.90	100%	100%	0
PG-T-CON-EXLS-HS-50_R	Install Recycled Precast Concrete Seats(Remaining)	10	31-Oct-26 08:00	10-Nov-26 17:00	30-Jul-26 08:00 A	07-Nov-26 14:36	0.00	54,123.39	60,137.10	0%	90%	-75
PG-T-CON-EXLS-HS-60	Install Recycled Precast Concrete Trash Bins	10	11-Nov-26 08:00	22-Nov-26 17:00	23-Sep-26 10:24 A	10-Nov-26 14:36	0.00	3,788.40	5,412.00	0%	70%	-31
SOFTSCAPE WORK		143	10-Jun-26 08:00	22-Nov-26 17:00	10-Jun-26 08:00 A	10-Nov-26 14:36	70,482.00	98,755.80	107,022.00	65.86%	92.28%	10
PG-T-CON-EXLS-SS-10	Planting Trees	12	10-Oct-26 08:00	22-Oct-26 17:00	22-Sep-26 08:00 A	05-Nov-26 14:36	46,122.00	41,509.80	46,122.00	100%	90%	-26
PG-T-CON-EXLS-SS-20	Lawn Area Preparation & Planting / Turfing(Completed)	13	10-Jun-26 08:00	24-Jun-26 17:00	10-Jun-26 08:00 A	24-Jun-26 17:00 A	24,360.00	24,360.00	24,360.00	100%	100%	0
PG-T-CON-EXLS-SS-20_R	Lawn Area Preparation & Planting / Turfing(Remaining)	6	16-Nov-26 08:00	22-Nov-26 17:00	12-Jul-26 08:00 A	10-Nov-26 14:36	0.00	32,886.00	36,540.00	0%	90%	-98
TANK WORKS		150	13-May-26 08:00	27-Sep-26 17:00	13-May-26 08:00 A	03-Nov-26 12:00	48,290.40	37,624.32	48,290.40	100%	77.91%	-32
SEPTIC TANK		146	13-May-26 08:00	03-Sep-26 17:00	13-May-26 08:00 A	01-Nov-26 17:00	7,475.22	7,223.04	7,475.22	100%	96.63%	-49
PG-T-CON-EXTW-ST-10	Excavation	21	13-May-26 08:00	10-Jun-26 17:00	13-May-26 08:00 A	10-Jun-26 17:00 A	252.18	252.18	252.18	100%	100%	0
PG-T-CON-EXTW-ST-20	PCC / Lean Concrete laying	27	20-May-26 08:00	24-Jun-26 17:00	20-May-26 08:00 A	24-Jun-26 17:00 A	168.12	168.12	168.12	100%	100%	0
PG-T-CON-EXTW-ST-30	RCC Foundation(Completed)	1	24-Jun-26 08:00	24-Jun-26 17:00	24-Jun-26 08:00 A	24-Jun-26 17:00 A	894.35	894.35	894.35	100%	100%	0
PG-T-CON-EXTW-ST-30_R	RCC Foundation(Remaining)	10	25-Jun-26 08:00	06-Jul-26 17:00	12-Jul-26 08:00 A	27-Aug-26 17:00 A	383.29	383.29	383.29	100%	100%	-31
PG-T-CON-EXTW-ST-40	RCC Wall	9	07-Jul-26 08:00	16-Jul-26 17:00	14-Aug-26 08:00 A	12-Oct-26 17:00 A	2,757.60	2,757.60	2,757.60	100%	100%	-41
PG-T-CON-EXTW-ST-50	RCC Slab	13	18-Jul-26 08:00	01-Aug-26 17:00	13-Oct-26 08:00 A	15-Oct-26 17:00 A	2,599.38	2,599.38	2,599.38	100%	100%	10
PG-T-CON-EXTW-ST-60	Finishing Work	8	18-Aug-26 08:00	26-Aug-26 17:00	24-Oct-26 08:00	01-Nov-26 17:00	252.18	0.00	252.18	100%	0%	0
PG-T-CON-EXTW-ST-70	Backfilling	7	27-Aug-26 08:00	03-Sep-26 17:00	20-Aug-26 08:00 A	24-Aug-26 17:00 A	168.12	168.12	168.12	100%	100%	3
WATER STORAGE TANK		150	13-May-26 08:00	27-Sep-26 17:00	13-May-26 08:00 A	03-Nov-26 12:00	40,815.18	30,401.28	40,815.18	100%	74.49%	-32
PG-T-CON-EXTW-IR-10	Excavation(Completed)	33	13-May-26 08:00	24-Jun-26 17:00	13-May-26 08:00 A	24-Jun-26 17:00 A	766.58	766.58	766.58	100%	100%	0
PG-T-CON-EXTW-IR-10_R	Excavation(Remaining)	6	29-Aug-26 08:00	03-Sep-26 17:00	08-Jul-26 08:00 A	09-Jul-26 17:00 A	85.18	85.18	85.18	100%	100%	4
PG-T-CON-EXTW-IR-20	RCC Foundation(Completed)	13	10-Jun-26 08:00	24-Jun-26 17:00	10-Jun-26 08:00 A	24-Jun-26 17:00 A	1,654.56	1,654.56	1,654.56	100%	100%	0
PG-T-CON-EXTW-IR-20_R	RCC Foundation(Remaining)	8	05-Sep-26 08:00	13-Sep-26 17:00	16-Jul-26 08:00 A	27-Aug-26 17:00 A	2,481.84	2,481.84	2,481.84	100%	100%	-29
PG-T-CON-EXTW-IR-30	Backfilling	6	14-Sep-26 08:00	20-Sep-26 17:00	14-Aug-26 08:00 A	25-Aug-26 17:00 A	1,114.02	1,114.02	1,114.02	100%	100%	-4
PG-T-CON-EXTW-IR-40	GRP Water Tank Installation	5	21-Sep-26 08:00	27-Sep-26 17:00	13-Oct-26 08:00 A	03-Nov-26 12:00	34,713.00	24,299.10	34,713.00	100%	70%	-14
AIR DOME CONSTRUCTION		220	13-May-26 08:00	03-Dec-26 17:00	13-May-26 08:00 A	30-Jan-27 17:00	3,110,229.58	1,210,693.39	4,178,041.20	74.44%	28.98%	-49
CIVIL WORK		152	13-May-26 08:00	14-Sep-26 17:00	13-May-26 08:00 A	11-Nov-26 17:00	1,711,669.97	1,210,693.39	1,711,669.97	100%	70.73%	-49
PG-T-CON-EXAD-CL-10	Excavation For Footing(Completed)	33	13-May-26 08:00	24-Jun-26 17:00	13-May-26 08:00 A	24-Jun-26 17:00 A	25,048.83	25,048.83	25,048.83	100%	100%	0
PG-T-CON-EXAD-CL-10_R	Excavation For Footing(Remaining)	7	05-Jul-26 08:00	12-Jul-26 17:00	08-Jul-26 08:00 A	10-Jul-26 17:00 A	225,439.46	225,439.46	225,439.46	100%	100%	5
PG-T-CON-EXAD-CL-20	Anti-Termite Treatment	1	13-Jul-26 08:00	13-Jul-26 17:00	10-Jul-26 08:00 A	10-Jul-26 17:00 A	83,496.10	83,496.10	83,496.10	100%	100%	1
PG-T-CON-EXAD-CL-30	PCC / Blinding Concrete	3	25-Jul-26 08:00	27-Jul-26 17:00	22-Jul-26 08:00 A	23-Jul-26 17:00 A	125,244.14	125,244.14	125,244.14	100%	100%	1
PG-T-CON-EXAD-CL-40	RCC Foundation Works	9	28-Jul-26 08:00	06-Aug-26 17:00	23-Jul-26 08:00 A	13-Aug-26 17:00 A	250,488.29	250,488.29	250,488.29	100%	100%	-10
PG-T-CON-EXAD-CL-50	Backfilling with Compaction	8	08-Aug-26 08:00	16-Aug-26 17:00	07-Aug-26 08:00 A	14-Aug-26 17:00 A	250,488.29	250,488.29	250,488.29	100%	100%	2
PG-T-CON-EXAD-CL-60	Installation of Anchorage System	8	17-Aug-26 08:00	25-Aug-26 17:00	27-Aug-26 08:00 A	23-Sep-26 09:36 A	250,488.29	250,488.29	250,488.29	100%	100%	-15
PG-T-CON-EXAD-CL-70	Installation of Steel Cable Structural System	9	26-Aug-26 08:00	05-Sep-26 17:00	24-Oct-26 08:00	02-Nov-26 17:00	250,488.29	0.00	250,488.29	100%	0%	0
PG-T-CON-EXAD-CL-80	Installation of Membrane System	8	06-Sep-26 08:00	14-Sep-26 17:00	03-Nov-26 08:00	11-Nov-26 17:00	250,488.29	0.00	250,488.29	100%	0%	0
ARCHITECTURAL WORK		25	05-Nov-26 08:00	03-Dec-26 17:00	02-Jan-27 08:00	30-Jan-27 17:00	0.00	0.00	712,953.22	0%	0%	0
PG-T-CON-EXAD-AR-10	Installation of Thermal Insulation System	7	05-Nov-26 08:00	12-Nov-26 17:00	02-Jan-27 08:00	09-Jan-27 17:00	0.00	0.00	250,488.29	0%	0%	0
PG-T-CON-EXAD-AR-20	Installation of Doors & Access Systems	6	22-Nov-26 08:00	28-Nov-26 17:00	18-Jan-27 08:00	24-Jan-27 17:00	0.00	0.00	250,488.29	0%	0%	0
PG-T-CON-EXAD-AR-30	Installation of Logo	5	29-Nov-26 08:00	03-Dec-26 17:00	25-Jan-27 08:00	30-Jan-27 17:00	0.00	0.00	3,236.40	0%	0%	0
PG-T-CON-EXAD-AR-40	Final Fixing of Accessories & Finishes	7	14-Nov-26 08:00	21-Nov-26 17:00	10-Jan-27 08:00	17-Jan-27 17:00	0.00	0.00	208,740.24	0%	0%	0
MECHANICAL WORK		23	15-Sep-26 08:00	12-Oct-26 17:00	12-Nov-26 08:00	08-Dec-26 17:00	667,968.77	0.00	667,968.77	100%	0%	0
PG-T-CON-EXAD-ME-10	Installation of Main Air Package Units	5	15-Sep-26 08:00	20-Sep-26 17:00	12-Nov-26 08:00	17-Nov-26 17:00	250,488.29	0.00	250,488.29	100%	0%	0
PG-T-CON-EXAD-ME-20	Installation of Backup Air Package Unit	5	21-Sep-26 08:00	27-Sep-26 17:00	18-Nov-26 08:00	23-Nov-26 17:00	208,740.24	0.00	208,740.24	100%	0%	0
PG-T-CON-EXAD-ME-30	Installation of Complete HVAC System	6	06-Oct-26 08:00	12-Oct-26 17:00	02-Dec-26 08:00	08-Dec-26 17:00	208,740.24	0.00	208,740.24	100%	0%	0
ELECTRICAL WORK		33	28-Sep-26 08:00	04-Nov-26 17:00	24-Nov-26 08:00	31-Dec-26 17:00	730,590.84	0.00	1,085,449.25	67.31%	0%	0
PG-T-CON-EXAD-EL-10	Installation of Electrical Boxes & MDBs	7	28-Sep-26 08:00	05-Oct-26 17:00	24-Nov-26 08:00	01-Dec-26 17:00	208,740.24	0.00	208,740.24	100%	0%	0
PG-T-CON-EXAD-EL-20	Installation of Lighting System	7	06-Oct-26 08:00	13-Oct-26 17:00	02-Dec-26 08:00	09-Dec-26 17:00	208,740.24	0.00	208,740.24	100%	0%	0
PG-T-CON-EXAD-EL-30	Electrical Connections to Main Power Source (Excluding kWh Meter)	5	14-Oct-26 08:00	19-Oct-26 17:00	10-Dec-26 08:00	15-Dec-26 17:00	208,740.24	0.00	208,740.24	100%	0%	0
PG-T-CON-EXAD-EL-40	Installation of Backup Generator	6	20-Oct-26 08:00	26-Oct-26 17:00	16-Dec-26 08:00	22-Dec-26 17:00	104,370.12	0.00	208,740.24	50%	0%	0
PG-T-CON-EXAD-EL-50	Installation of Smart Dome System	8	27-Oct-26 08:00	04-Nov-26 17:00	23-Dec-26 08:00	31-Dec-26 17:00	0.00	0.00	250,488.29	0%	0%	0
TOILET BUILDING WORKS		143	12-May-26 08:00	28-Oct-26 17:00	12-May-26 08:00 A	28-Oct-26 11:12	315,130.32	305,167.32	324,844.38	97.01%	93.94%	1
CIVIL WORK		143	12-May-26 08:00	26-Oct-26 17:00	12-May-26 08:00 A	27-Oct-26 12:48	217,539.78	221,677.98	227,117.58	95.78%	97.6%	-1
STRUCTURAL WORK		59	12-May-26 08:00	01-Aug-26 17:00	12-May-26 08:00 A	12-Aug-26 17:00 A	37,980.00	37,980.00	37,980.00	100%	100%	-10
PG-T-CON-B-STR-10	Excavation up to bottom of footing	2	12-May-26 08:00	13-May-26 17:00	12-May-26 08:00 A	13-May-26 17:00 A	1,900.80	1,900.80	1,900.80	100%	100%	0
PG-T-CON-B-STR-20	Anti-termite treatment and Polyethene Sheet	2	12-May-26 08:00	13-May-26 17:00	12-May-26 08:00 A	13-May-26 17:00 A	3,294.00	3,294.00	3,294.00	100%	100%	0
PG-T-CON-B-STR-30	Backfilling with selected fill material (under footing)	1	13-May-26 08:00	13-May-26 17:00	13-May-26 08:00 A	13-May-26 17:00 A	1,900.80	1,900.80	1,900.80	100%	100%	0
PG-T-CON-B-STR-40	Raft Foundation Work	27	13-May-26 08:00	17-Jun-26 17:00	13-May-26 08:00 A	17-Jun-26 17:00 A	2,534.40	2,534.40	2,534.40	100%	100%	0
PG-T-CON-B-STR-50	Autoclaved aerated panel (walls)	9	07-Jul-26 08:00	16-Jul-26 17:00	07-Jul-26 08:00 A	09-Jul-26 17:00 A	11,340.00	11,340.00	11,340.00	100%	100%	6
PG-T-CON-B-STR-60	Autoclaved aerated panel (ceiling)	9	18-Jul-26 08:00	27-Jul-26 17:00	09-Jul-26 08:00 A	31-Jul-26 17:00 A	8,505.00	8,505.00	8,505.00	100%	100%	-10
PG-T-CON-B-STR-70	Autoclaved aerated panel (parapet)	4	28-Jul-26 08:00	01-Aug-26 17:00	11-Jul-26 08:00 A	12-Aug-26 17:00 A	8,505.00	8,505.00	8,505.00	100%	100%	-25
ARCHITECTURAL WORK		76	02-Aug-26 08:00	26-Oct-26 17:00	01-Aug-26 08:00 A	27-Oct-26 12:48	179,559.78	183,697.98	189,137.58	94.94%	97.12%	-2
GENERAL FINISHES		76	02-Aug-26 08:00	21-Oct-26 17:00	01-Aug-26 08:00 A	07-Sep-26 09:36 A	84,120.00	84,120.00	84,120.00	100%	100%	37
PG-T-CON-B-ARGF-10	Block Works	6	02-Aug-26 08:00	08-Aug-26 17:00	01-Aug-26 08:00 A	06-Aug-26 17:00 A	2,484.00	2,484.00	2,484.00	100%	100%	0
PG-T-CON-B-ARGF-20	Plaster	7	18-Aug-26 08:00	25-Aug-26 17:00	06-Aug-26 08:00 A	07-Aug-26 17:00 A	4,427.40	4,427.40	4,427.40	100%	100%	6

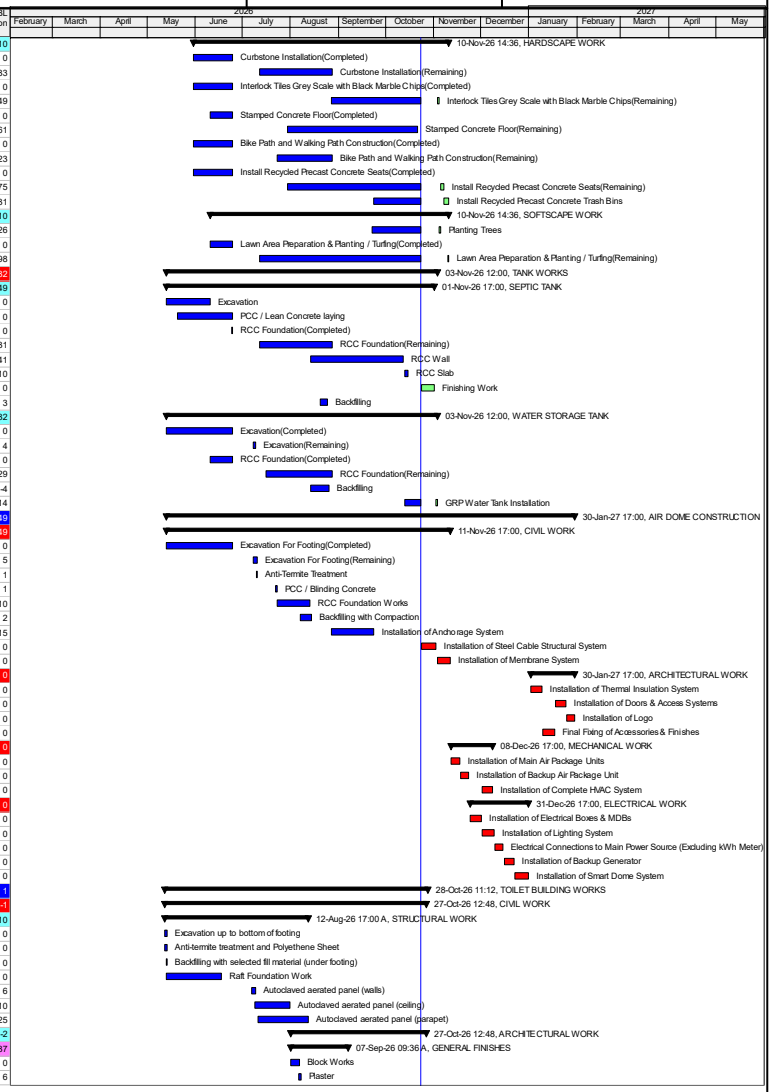

Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining W...
Milestone
summary

Baseline Schedule Rev.00

PLAYGROUNDS INITIATIVE - QASSIM, HAIL & TABUK - 25-Oct-2026

Activity ID	Activity Name	O.D	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Schedule % Complete	Performance % Complete	Variance - BL Project Duration
PG-T-CON-B-ARGF-30	False Ceiling Installation & Finishing	8	26-Aug-26 08:00	03-Sep-26 17:00	20-Aug-26 08:00 A	07-Sep-26 09:36 A	873.60	873.60	873.60	100%	100%	-7
PG-T-CON-B-ARGF-40	Wall Paint	10	19-Sep-26 08:00	30-Sep-26 17:00	20-Aug-26 08:00 A	07-Sep-26 09:36 A	2,958.00	2,958.00	2,958.00	100%	100%	-5
PG-T-CON-B-ARGF-50	Epoxy Flooring	7	01-Oct-26 08:00	08-Oct-26 17:00	20-Aug-26 08:00 A	07-Sep-26 09:36 A	273.60	273.60	273.60	100%	100%	-8
PG-T-CON-B-ARGF-60	Install Doors & Windows	4	10-Oct-26 08:00	13-Oct-26 17:00	27-Aug-26 08:00 A	07-Sep-26 09:36 A	13,273.80	13,273.80	13,273.80	100%	100%	-5
PG-T-CON-B-ARGF-70	Lockers and Furniture Installation	2	20-Oct-26 08:00	21-Oct-26 17:00	27-Aug-26 08:00 A	07-Sep-26 09:36 A	7,551.60	7,551.60	7,551.60	100%	100%	-7
PG-T-CON-B-ARGF-80	Facade Finishing Work	9	10-Oct-26 08:00	19-Oct-26 17:00	20-Aug-26 08:00 A	07-Sep-26 09:36 A	52,278.00	52,278.00	52,278.00	100%	100%	-6
WET AREA FINISHES		37	26-Aug-26 08:00	13-Oct-26 17:00	06-Aug-26 08:00 A	26-Oct-26 08:48	81,123.78	79,515.30	81,123.78	100%	98.02%	-27
PG-T-CON-B-ARWF-10	False Ceiling Installation & Finishing	4	26-Aug-26 08:00	30-Aug-26 17:00	20-Aug-26 08:00 A	10-Sep-26 12:48 A	2,898.00	2,898.00	2,898.00	100%	100%	-15
PG-T-CON-B-ARWF-20	Wall Tiles and Partition Work	3	01-Oct-26 08:00	04-Oct-26 17:00	06-Aug-26 08:00 A	14-Aug-26 17:00 A	21,283.20	21,283.20	21,283.20	100%	100%	-4
PG-T-CON-B-ARWF-30	Waterproofing on Floor	2	05-Oct-26 08:00	06-Oct-26 17:00	14-Aug-26 08:00 A	10-Sep-26 12:48 A	5,784.00	5,784.00	5,784.00	100%	100%	-22
PG-T-CON-B-ARWF-40	Floor Tiles Works	3	07-Oct-26 08:00	10-Oct-26 17:00	14-Aug-26 08:00 A	10-Sep-26 12:48 A	6,489.00	6,489.00	6,489.00	100%	100%	-21
PG-T-CON-B-ARWF-50	Toilet accessories Installation Works	3	11-Oct-26 08:00	13-Oct-26 17:00	20-Aug-26 08:00 A	10-Sep-26 12:48 A	39,307.98	39,307.98	39,307.98	100%	100%	-16
PG-T-CON-B-ARWF-60	Install Doors	2	11-Oct-26 08:00	12-Oct-26 17:00	23-Sep-26 11:12 A	26-Oct-26 08:48	5,361.60	3,753.12	5,361.60	100%	70%	-25
ROOF FINISHES		46	07-Oct-26 08:00	26-Oct-26 17:00	14-Aug-26 08:00 A	27-Oct-26 12:48	14,316.00	20,062.68	23,893.80	59.92%	83.97%	-46
PG-T-CON-B-ARRF-10	Waterproofing on Floor	7	07-Oct-26 08:00	14-Oct-26 17:00	14-Aug-26 08:00 A	12-Sep-26 14:36 A	4,158.00	4,158.00	4,158.00	100%	100%	-18
PG-T-CON-B-ARRF-20	Epoxy Flooring and Finishes	7	15-Oct-26 08:00	22-Oct-26 17:00	20-Aug-26 08:00 A	12-Sep-26 14:36 A	10,158.00	10,158.00	10,158.00	100%	100%	-13
PG-T-CON-B-ARRF-30	Steel ladder and Steel roof scupper Installation	3	24-Oct-26 08:00	26-Oct-26 17:00	19-Sep-26 11:12 A	27-Oct-26 12:48	0.00	5,746.68	9,577.80	0%	60%	-29
MEP WORK		103	16-Jun-26 08:00	28-Oct-26 17:00	16-Jun-26 08:00 A	28-Oct-26 11:12	97,590.54	83,489.34	97,726.80	99.86%	85.43%	1
MECANICAL WORKS		103	16-Jun-26 08:00	28-Oct-26 17:00	16-Jun-26 08:00 A	28-Oct-26 11:12	79,343.22	65,242.02	79,479.48	99.83%	82.09%	1
FIRE FIGHTING SYSTEM		2	27-Oct-26 08:00	28-Oct-26 17:00	23-Sep-26 11:12 A	28-Oct-26 11:12	0.00	81.76	136.26	0%	60%	-27
PG-T-CON-B-GF-FF-10	Fire Extinguisher Installation	2	27-Oct-26 08:00	28-Oct-26 17:00	23-Sep-26 11:12 A	28-Oct-26 11:12	0.00	81.76	136.26	0%	60%	-27
SEWER AND DRAINAGE SYSTEM		92	16-Jun-26 08:00	05-Sep-26 17:00	16-Jun-26 08:00 A	25-Oct-26 12:00	11,290.02	10,322.30	11,290.02	100%	91.43%	-42
PG-T-CON-B-GF-DR-10	Sewer and Drainge System Main Lines Installation(Completed)	8	16-Jun-26 08:00	24-Jun-26 17:00	16-Jun-26 08:00 A	24-Jun-26 17:00 A	967.72	967.72	967.72	100%	100%	0
PG-T-CON-B-GF-DR-10_R	Sewer and Drainge System Main Lines Installation(Remaining)	1	12-Aug-26 08:00	13-Aug-26 17:00	23-Jul-26 08:00 A	10-Sep-26 09:36 A	2,258.00	2,258.00	2,258.00	100%	100%	-40
PG-T-CON-B-GF-DR-20	Sewer and Drainge System Pipes and fittings Installation(Completed)	8	16-Jun-26 08:00	24-Jun-26 17:00	16-Jun-26 08:00 A	24-Jun-26 17:00 A	1,451.57	1,451.57	1,451.57	100%	100%	0
PG-T-CON-B-GF-DR-20_R	Sewer and Drainge System Pipes and fittings Installation(Remaining)	1	15-Aug-26 08:00	16-Aug-26 17:00	23-Jul-26 08:00 A	31-Jul-26 17:00 A	3,387.01	3,387.01	3,387.01	100%	100%	-5
PG-T-CON-B-GF-DR-30	Sanitaryware Installation (Final Fix)	2	03-Sep-26 08:00	05-Sep-26 17:00	23-Sep-26 08:00 A	25-Oct-26 12:00	3,225.72	2,258.00	3,225.72	100%	70%	-25
HVAC SYSTEM		42	09-Aug-26 08:00	12-Oct-26 17:00	13-Aug-26 08:00 A	26-Oct-26 08:48	12,127.20	9,821.76	12,127.20	100%	80.99%	-7
PG-T-CON-B-GF-AC-10	Duct Work and Exhaust Fan Installation	3	09-Aug-26 08:00	11-Aug-26 17:00	13-Aug-26 08:00 A	20-Aug-26 17:00 A	4,442.40	4,442.40	4,442.40	100%	100%	-4
PG-T-CON-B-GF-AC-20	Split AC, Grills & Diffuser Installation	2	11-Oct-26 08:00	12-Oct-26 17:00	20-Sep-26 08:00 A	26-Oct-26 08:48	7,684.80	5,379.36	7,684.80	100%	70%	-28
WATER SUPPLY SYSTEM		45	12-Aug-26 08:00	02-Sep-26 17:00	22-Jul-26 08:00 A	24-Oct-26 16:12	55,926.00	45,016.20	55,926.00	100%	80.49%	-61
PG-T-CON-B-GF-WS-10	Water Supply Main Lines Installation	2	12-Aug-26 08:00	13-Aug-26 17:00	22-Jul-26 08:00 A	10-Sep-26 09:36 A	5,702.40	5,702.40	5,702.40	100%	100%	-41
PG-T-CON-B-GF-WS-20	Water Supply Pipes Installation (Cold and Hot Water)	2	15-Aug-26 08:00	16-Aug-26 17:00	23-Jul-26 08:00 A	30-Jul-26 17:00 A	13,857.60	13,857.60	13,857.60	100%	100%	-5
PG-T-CON-B-GF-WS-30	Water Supply Accesories and Booster pump Installation	3	31-Aug-26 08:00	02-Sep-26 17:00	23-Sep-26 08:00 A	24-Oct-26 16:12	36,366.00	25,456.20	36,366.00	100%	70%	-23
ELECTRICAL WORKS		38	15-Aug-26 08:00	17-Sep-26 17:00	22-Jul-26 08:00 A	16-Sep-26 10:24 A	18,247.32	18,247.32	18,247.32	100%	100%	-18
PG-T-CON-B-GF-EL-10	Pipes & Conduits Installation	3	15-Aug-26 08:00	17-Aug-26 17:00	22-Jul-26 08:00 A	23-Jul-26 17:00 A	1,983.60	1,983.60	1,983.60	100%	100%	1
PG-T-CON-B-GF-EL-20	Electrical & ELV Wiring Works	3	15-Sep-26 08:00	17-Sep-26 17:00	20-Aug-26 08:00 A	16-Sep-26 10:24 A	1,983.60	1,983.60	1,983.60	100%	100%	-20
PG-T-CON-B-GF-EL-30	Fire Alarm Devices Installation	3	08-Sep-26 08:00	10-Sep-26 17:00	20-Aug-26 08:00 A	16-Sep-26 10:24 A	1,983.60	1,983.60	1,983.60	100%	100%	-20
PG-T-CON-B-GF-EL-40	Telecom & CCTV Devices Installation	3	12-Sep-26 08:00	14-Sep-26 17:00	20-Aug-26 08:00 A	16-Sep-26 10:24 A	4,959.00	4,959.00	4,959.00	100%	100%	-20
PG-T-CON-B-GF-EL-50	Electrical Light Fixtures Installation	2	06-Sep-26 08:00	07-Sep-26 17:00	20-Aug-26 08:00 A	16-Sep-26 10:24 A	7,337.52	7,337.52	7,337.52	100%	100%	-21
PROJECT CLOSOUT		221	25-May-26 08:00	16-Dec-26 17:00	25-May-26 08:00 A	11-Feb-27 17:00	34,073.40	210,119.32	1,135,780.10	3%	18.5%	-49
PG-T-PCL-10	Testing, Commissioning for All Systems(Completed)	23	25-May-26 08:00	24-Jun-26 17:00	25-May-26 08:00 A	24-Jun-26 17:00 A	34,073.40	34,073.40	34,073.40	100%	100%	0
PG-T-PCL-10_R	Testing, Commissioning for All Systems(Remaining)	11	22-Nov-26 08:00	03-Dec-26 17:00	06-Aug-26 08:00 A	30-Jan-27 17:00	0.00	153,330.31	306,660.63	0%	50%	-140
PG-T-PCL-20	As-Built Drawings	15	22-Nov-26 08:00	08-Dec-26 17:00	23-Sep-26 11:02 A	07-Feb-27 12:48	0.00	22,715.60	113,578.01	0%	20%	-102
PG-T-PCL-30	Snag list Submission	2	05-Dec-26 08:00	06-Dec-26 17:00	31-Jan-27 08:00	01-Feb-27 17:00	0.00	0.00	227,156.02	0%	0%	0
PG-T-PCL-40	Snag list Closeout	7	07-Dec-26 08:00	14-Dec-26 17:00	02-Feb-27 08:00	09-Feb-27 17:00	0.00	0.00	227,156.02	0%	0%	0
PG-T-PCL-50	Issuing Approvals	1	15-Dec-26 08:00	15-Dec-26 17:00	10-Feb-27 08:00	10-Feb-27 17:00	0.00	0.00	113,578.01	0%	0%	0
PG-T-PCL-60	Handing Over	1	16-Dec-26 08:00	16-Dec-26 17:00	11-Feb-27 08:00	11-Feb-27 17:00	0.00	0.00	113,578.01	0%	0%	0



Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining W...
Milestone
summary

Baseline Schedule Rev.00
