Development of Infrastructure Networks, Al-Kharj Industrial City

تطوير شبكات البنية التحتية بالمدينة الصناعية بالخرج

CLIENT	CONTRACTOR	CONSULTANT	MODON PM	SITE HANDOVER	CONTRACT COMPLETION
MODON	Moffreh Group (MMAH)	EGIS	Rakan Alotaibi	03-Dec-2025	02-Dec-2027

Scope: infrastructure networks over about 3.5 km² in Zones A and B and the Labour Community Area, around 100 km south-east of Riyadh.

Status at a glance

Progress is measured as physical % complete, weighted by budgeted man-hours. Against the revised plan issued on 26 Oct, the project is 0.6% ahead: 50.4% complete against 49.8% planned, after gaining 1.2% this week against 0.75% planned.

PHYSICAL % COMPLETE

50.4% / 49.8% plan

▲ SPI 1.01 +0.6 pts

PROGRESS THIS WEEK

+1.2 pts / +0.75 plan

▲ 0.4 pts above the weekly plan

CONTRACT TIME ELAPSED

45.8% · day 334 of 730

● P6 finish 02-Dec-2027

INVOICED TO DATE (GROSS)

18.6% · 49.7M SAR

5 invoices, last period ends 30-Sep-2026

The finish date is back on the contract date, but the road and MV milestones are three to four months late.

The P6 update uploaded this week (data date 03-Nov-2026) finishes the project on 02-Dec-2027 with zero float, against 27-Apr-2028 in last week's file. Road works are forecast for 02-Jan-2027 and the MV network for 08-Feb-2027, 92 and 129 days after their baseline dates, and asphalt works now face a stoppage because of bitumen supply constraints. Against the original baseline, which called for 83.0% by the end of October, the project remains far behind at 50.4%.

Site photos this week

Six photos from the 02-Nov-2026 weekly report workbook; one is GPS-stamped 31-Oct-2026. Asphalt paving continues, curbstones and street lighting fixtures are being installed, and block masonry is progressing. Select a photo to view it larger, then use the arrows to move between photos.



Asphalt paving crew

Paver and crew laying asphalt. GPS-stamped 31-Oct-2026, 07:14.



Asphalt paving

Two pavers laying a fresh asphalt layer.




Asphalt supply and rolling

Truck delivering asphalt with a roller working ahead.




Curbstone installation

Curbstones set along a median, with compaction between the curbs.

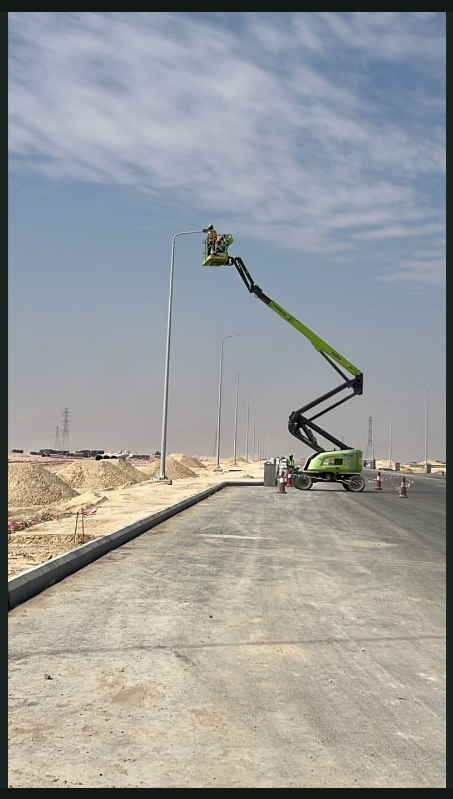

Street lighting fixtures

Boom lift fitting a luminaire to a lighting pole.

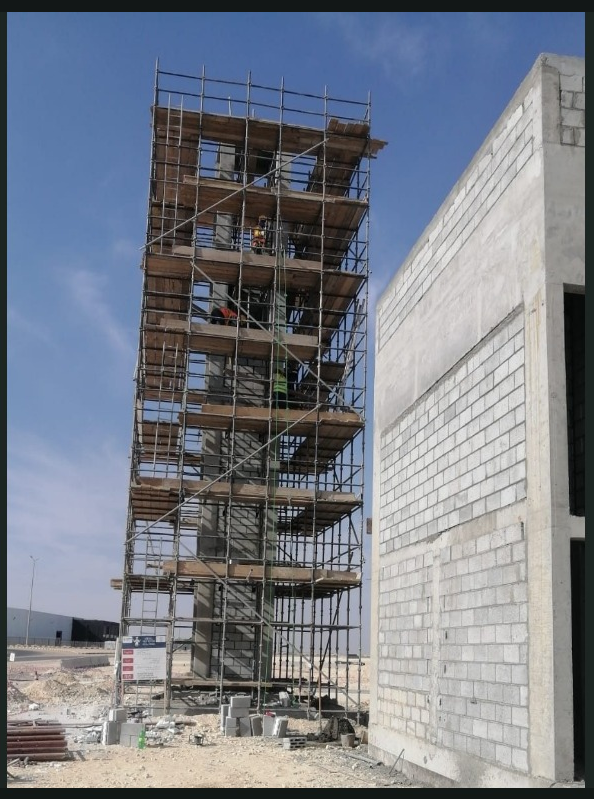


Block masonry

Scaffolded concrete tower beside a block masonry wall.

Progress S-curve

Cumulative physical progress (man-hour weighted), monthly. Source: Physical-Chart Data sheet.

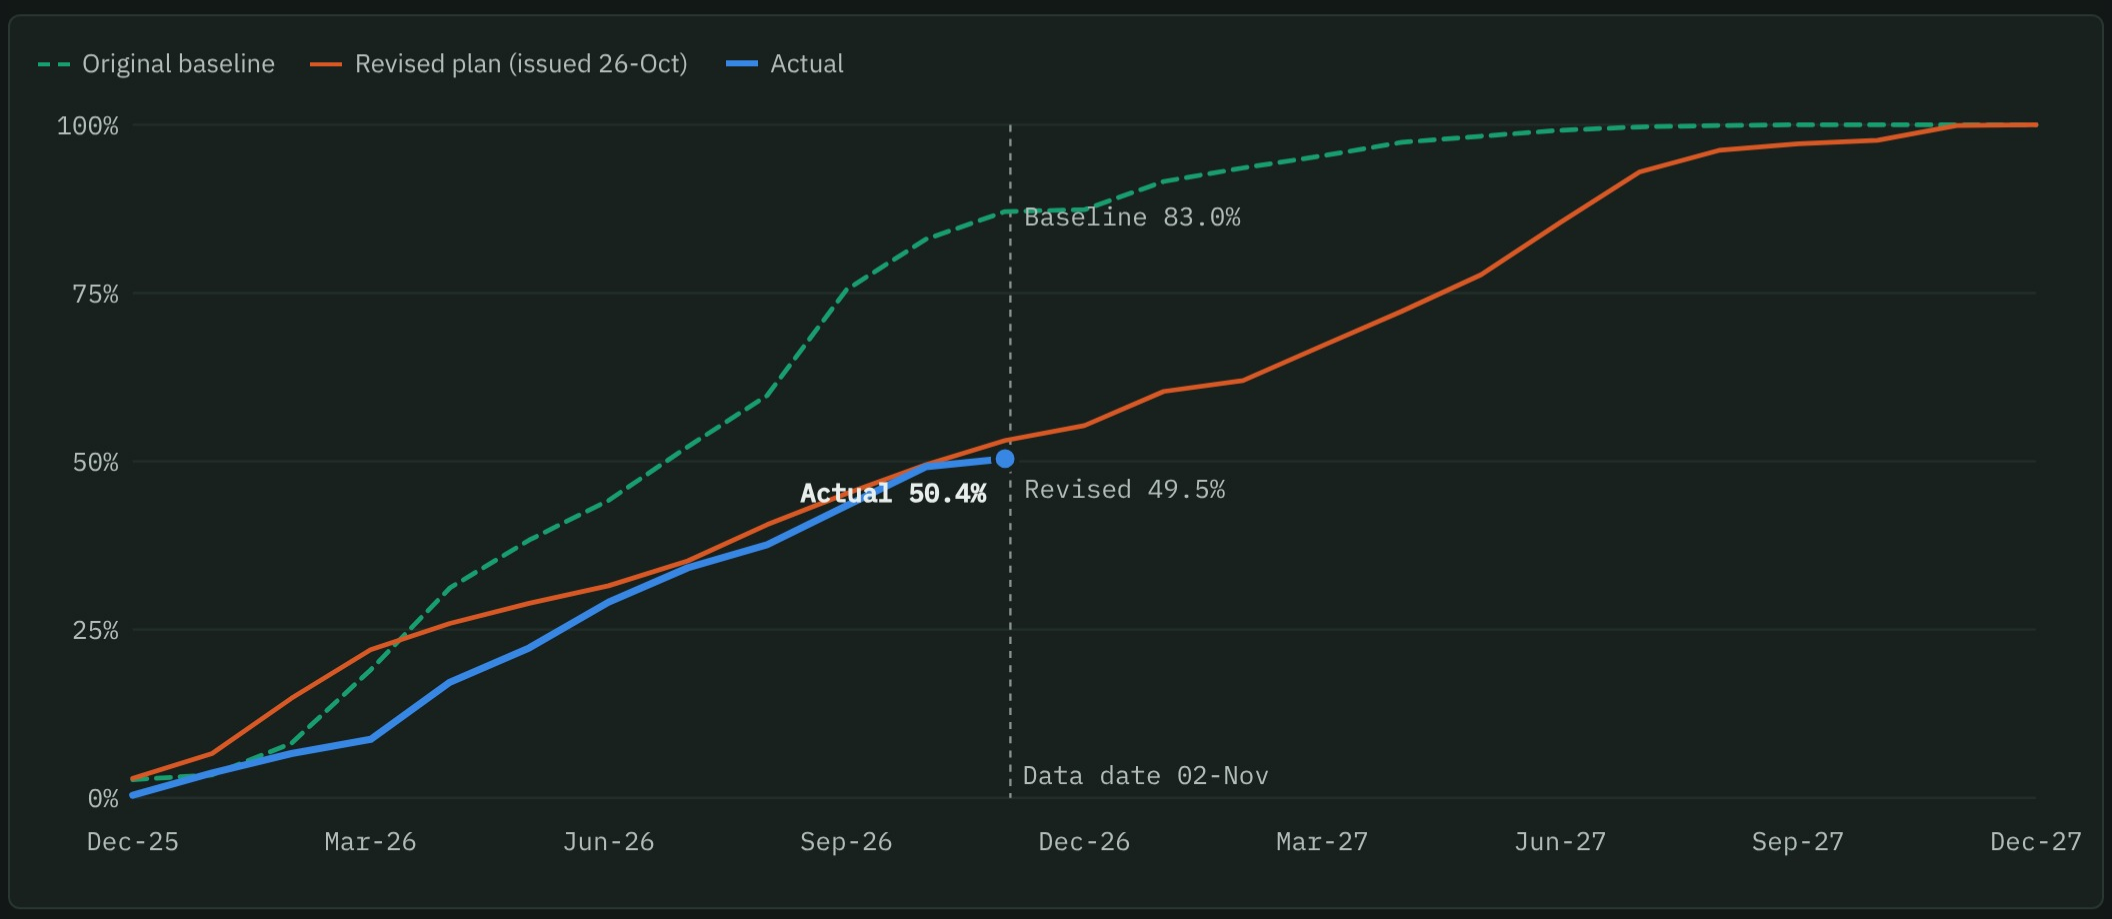

WEEK ENDING	PLANNED %	ACTUAL %	VARIANCE	GAINED THIS WEEK	SPI
28-Sep-2026	47.2	42.5	−4.7	+0.8	0.90
05-Oct-2026	50.1	43.4	−6.7	+0.9	0.87
12-Oct-2026	51.4	45.7	−5.7	+2.3	0.89
19-Oct-2026	52.5	47.0	−5.5	+1.3	0.89
26-Oct-2026	48.4*	49.3	+0.9	+2.2	1.02
02-Nov-2026	**49.8**	**50.4**	**+0.6**	**+1.2**	**1.01**

Physical % complete from the weekly reports for 28 Sep to 02 Nov. * From 26 Oct the planned value comes from the revised plan issued that week. This week the cumulative plan rose by 1.4%, while the effort table gives 0.75% as this week's planned progress.

Progress by phase


Physical progress to date by WBS, weighted by budgeted man-hours.

PHASE	WEIGHT	PLANNED	ACTUAL	VARIANCE	SPI	STATUS
Engineering	3%	100.0%	100.0%	0.0	1.00	✓ Complete
Procurement	20%	69.0%	77.7%	+8.7	1.13	▲ Ahead
Construction	67%	46.9%	47.6%	+0.7	1.01	▲ On track
Testing & commissioning	10%	16.0%	0.0%	−16.0	0.00	▼ Not started
Total	100%	**49.8%**	**50.4%**	**+0.6**	**1.01**	▲ On track

The P6 update (schedule ICKM01-22.Oct.2026-1, data date 03-Nov-2026) has 5,877 activities: 3,718 completed, 258 in progress and 1,901 not started. Its scheduled finish is 02-Dec-2027, the contract date.

Scope of work: quantities

No progress presentation was uploaded this week, so the per-network quantity tables are not available. This section shows the major quantity tracker in the 02-Nov-2026 weekly report (Zones A and B combined). "This week" is the change since the 26-Oct-2026 presentation, which uses the same totals; asphalt is tracked in tonnes, so it has no comparison.

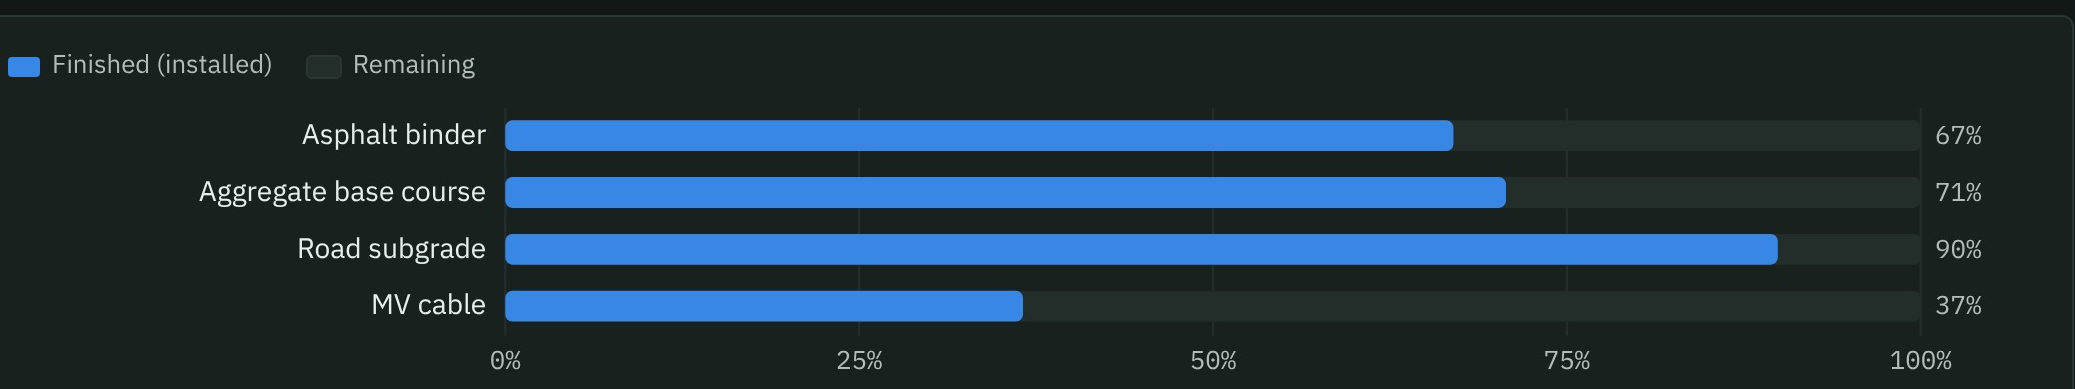

SCOPE ITEM	ZONE	UNIT	TOTAL	FINISHED	THIS WEEK	REMAINING	% FINISHED	BACKFILLED
Asphalt binder	A + B	t	110,480	74,008	–	36,472	67.0%	–
Aggregate base course	A + B	m³	99,916	70,640	+321	29,276	70.7%	–
Road subgrade	A + B	m³	160,925	144,678	0	16,247	89.9%	–
MV cable	A + B	LM	72,000	26,337	0	45,663	36.6%	–

All four tracked items were due by now

The tracker's plan to date equals the full quantity for every item. Still remaining: 36,472 t of asphalt binder, 29,276 m³ of aggregate base, 16,247 m³ of subgrade and 45,663 LM of MV cable.

Subgrade and MV unchanged

Subgrade (144,678 m³) and MV cable (26,337 LM) match the 26-Oct presentation exactly, so either no work was recorded this week or the tracker was not updated. Aggregate base gained 321 m³.

Milestones

The weekly report and the P6 update now give the same forecasts for road works and the MV network. The other interim milestones come from P6 only.

MILESTONE	BASELINE	WEEKLY REPORT FORECAST	P6 UPDATE FORECAST	P6 FLOAT (DAYS)	STATUS
Site handover	03-Dec-2025	03-Dec-2025	03-Dec-2025 (actual)	–	✓ Done
Complete mobilisation	02-Jan-2026	02-Jan-2026	–	–	✓ Done
Road works	02-Oct-2026	02-Jan-2027 (+92 d)	02-Jan-2027	−79	▼ Late

MILESTONE	BASELINE	WEEKLY REPORT FORECAST	P6 UPDATE FORECAST	P6 FLOAT (DAYS)	STATUS
Medium-voltage network	02-Oct-2026	08-Feb-2027 (+129 d)	08-Feb-2027	−110	▼ Late
Sewage network	–	–	28-Feb-2027	−22	▼ At risk
Storm network	–	–	16-Mar-2027	−35	▼ At risk
Irrigation network	–	–	27-Mar-2027	−44	▼ Late
Potable water network	–	–	29-Mar-2027	−46	▼ Late
Telecom network	–	–	26-May-2027	−95	▼ Late
All networks	02-Feb-2027	29-Mar-2027 (+55 d)	–	–	▼ Late
Landscape	–	–	04-Oct-2027	+51	● On track
Project handover	02-Dec-2027	02-Dec-2027	02-Dec-2027	0	● No float

The P6 telecom date conflicts with the weekly report's "All networks" forecast of 29-Mar-2027.

P6 finishes the telecom network on 26-May-2027 with −95 days of float. Open activities with negative float fell from 1,243 to 574, led by bituminous construction (20), aggregate base course (19) and earthworks (17). The worst float, −110 days, sits on the MV works and on the asphalt binder and base course chain. Last week's file finished the project on 27-Apr-2028; the contractor should explain the logic and duration changes behind the 147-day recovery.

Procurement of key materials

Share of total quantity delivered to site. Source: Procurement sheet, weekly report 02-Nov-2026.



Interlock paving: 3% delivered


4,280 of 129,381 LM, up 500 this week, although the sheet still says the sample is not approved and supply is on hold.

Valves, ICT manholes and planting

Sluice valves 347 of 2,723 delivered (13%). ICT manholes 0 of 214, due by 20-Nov. Planting (30,556 m²) waits for the final quantity to be agreed. MV cable is still at 61 of 72 km, waiting for SEC to waive the factory acceptance test. Curbstone (+2,200 LM), DI covers (+200) and box culverts (+50 LM) advanced this week.

Manpower

Monthly head count on site, planned vs actual. Source: Manpower sheet.

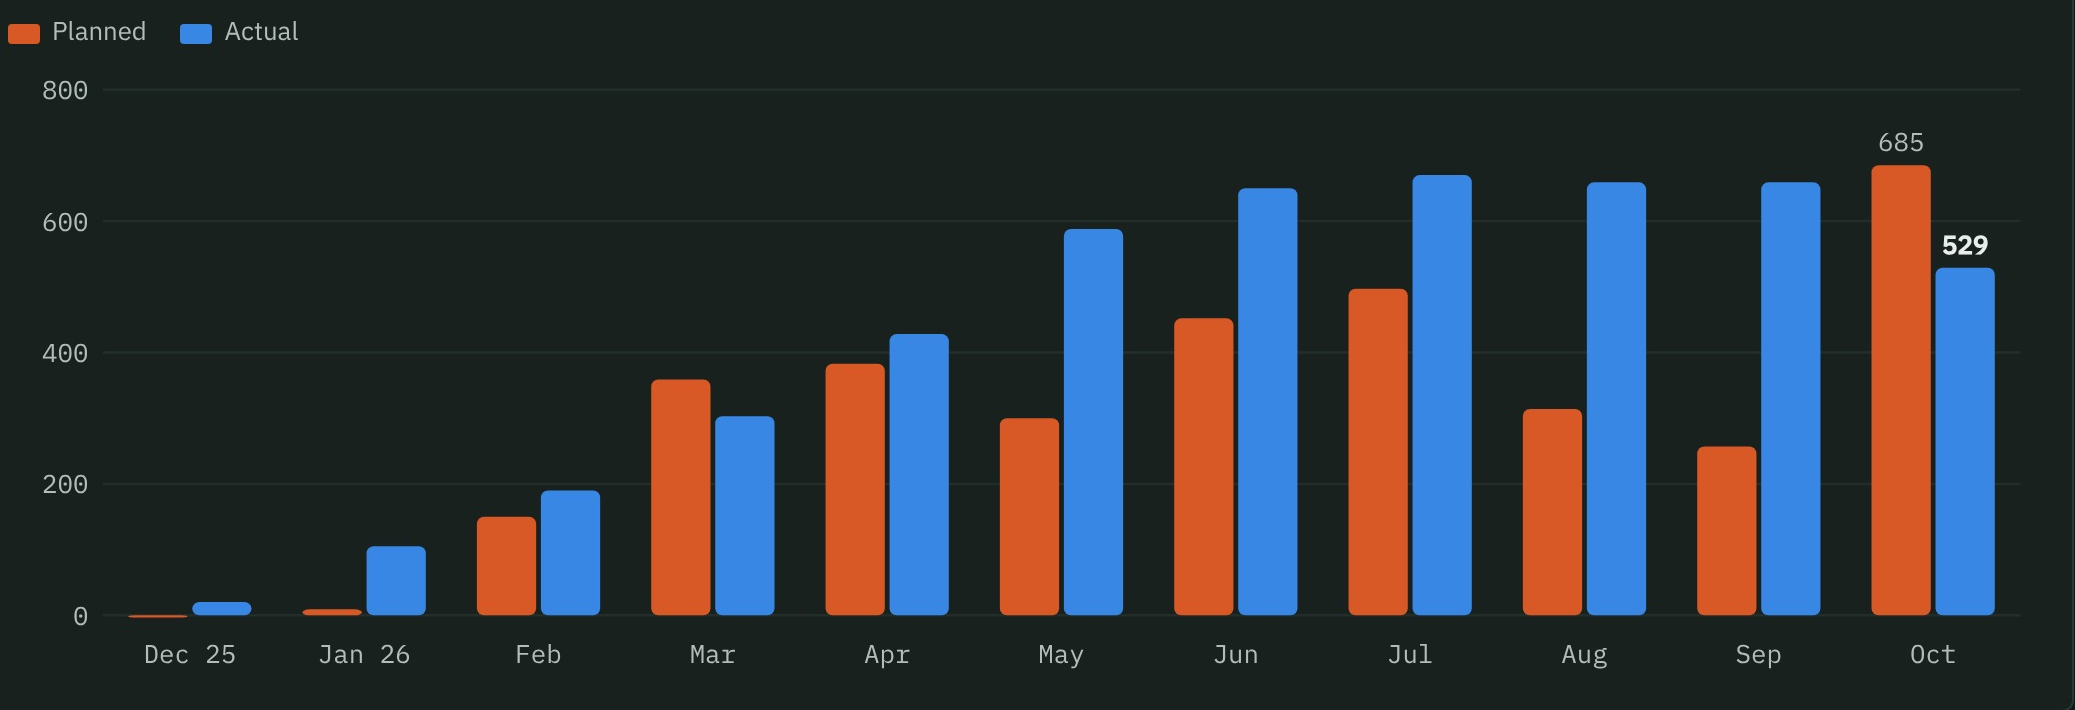

October head count is 529 against 685 planned (–23%). The 02-Nov report repeats the October figure again and has no November count yet. The planned head count was replaced this week: October rose from 677 to 685 and the November peak fell from 841 to 721.

Cost and invoicing

Contract value

Package 01: infrastructure, 3.5 km²	226,527,683
Package 02: Labour Camp area	18,085,168
Package 03: mosque, helipad, stormwater, road rehab	23,118,731
BOQ total (excl. VAT)	**267,731,582**
Contract value incl. 15% VAT	307,891,320
Change orders	0

All values in SAR. The BOQ total plus 15% VAT matches the contract value. No change orders are registered.

Invoices

Invoices submitted	5
Gross value	49,710,656
Retention (10%)	4,971,066
Deductions and penalties	111,000
Net incl. VAT	51,339,529
FIR value to date	67,676,799

Invoicing is 18.6% of the BOQ value excluding VAT (16.1% of the contract value including VAT) against 50.4% physical progress. The FIR value rose by 5,966,143 this week. The invoice summary still shows 0 submitted, approved and paid invoices, so the payment status needs confirming.

Health, safety and quality

Safety Score 0.90

Safe man-hours (cumulative)	1,172,525
Man-hours this week	37,080
Lost-time injuries	0
Fatalities	0
First-aid cases	6
Near misses	2
Property damage	3
Inductions / toolbox talks	1,959 / 218

Quality Score 0.93

FIRs this week: approved	327
FIRs this week: rejected	7
FIRs under review	49
Tests performed (cumulative)	2,544
NCRs issued (cumulative)	42
RFIs open / closed	4 / 124
MIRs approved this week	5
Approved shop drawings	2,087

Quality week: 24–31 Oct 2026. Five NCRs and 20 rejected shop drawings were recorded this week.

Open issues and risks

ISSUE	OWNER	DETAIL
Bitumen supply	Contractor	Asphalt works face a stoppage because of bitumen supply constraints; the contractor reports that Aramco has closed the Ras Tanura and Riyadh refineries.
Box conduit, existing utilities	Client / Consultant	Excavation for the box conduit is constrained because the existing underground utilities are not adequately shown in the as-built records. Verified utility information is needed.
Box culvert, Zone A	Contractor	Excavation for the stormwater box culvert conflicts with existing LV/MV cables and water and irrigation pipelines.
MV network clashes	Contractor	The MV route runs too close to the water and irrigation networks, which is preventing internal MV works from starting.
Cost savings	Contractor	Identify and use potential financial and technical savings.

The issue log now marks site obstacles, milestone recovery and GRP raw material supply as closed. Open risks in the register: weather (rain, wind, dust), supply of subgrade fill, manholes and pipes, deep excavation safety, existing services and roads, and delays in key materials.

Data notes

- No progress presentation was uploaded with the 02-Nov report, so quantities by network and zone, and this week's installed quantities, are not available. The scope section uses the weekly report's four-item quantity tracker.
- The P6 finish moved from 27-Apr-2028 to 02-Dec-2027 in one update, the potable water float from −230 to −46 days and the open negative-float activities from 1,243 to 574. Several in-progress street lighting and curbstone activities still run to 09-Oct-2028, after the project finish, which points to open-ended logic.
- The main summary sheet shows the milestone forecasts as the baseline dates, while its own days-change column and the Milestones sheet give −92, −129 and −55 days. The consultant's comment sheet at the front of the PDF raises the same point.
- The cumulative plan rose from 48.4% to 49.8% this week, while the effort table gives 0.75% as this week's planned progress.
- The manpower plan was replaced (October 677 → 685, November 841 → 721), and the actual October figure of 529 is repeated for the third report with no November count.
- The weekly report now measures cost against 267,731,582 SAR excluding VAT instead of 307,891,320 SAR, so invoiced to date reads 18.6% instead of 16.1%; the Invoice Log still uses the old value. "Penalties & retention" in the summary now shows 111,000 only, without the 4,971,066 retention.
- Quality: approved MIRs show 5 cumulative (49 last week), so the counter was reset again; cumulative shop drawings read 20,887 instead of 2,087; NCRs this week are 5 in Quality-Stat but 4 in Weekly Quality. The Quality-Stat sheet also reports cost-based progress as "actual"; it is not used here.
- The summary panel's FIR counts (353 issued, 294 closed) repeat last week's figures; the Weekly Quality sheet gives 407 FIRs received this week.
- Procurement notes still say several items finish delivery on 20 Oct (storm manholes, box culverts, sluice valves, MV cable) although they are incomplete, and interlock deliveries rose although supply is recorded as on hold.
- The SPI sheet labels the new week "Week 5 26.Oct.2026" again, and the HSE "this month" man-hours (131,580) still include October.

Compiled 05-Nov-2026 from the weekly reports uploaded for weeks ending 28 Sep to 02 Nov 2026.
