
MLTX-02-005 - Playground Initiative for Eastern Region (Arar-Hasa osis -Dammam)

2 Weeks look ahead schedule
D.D 19-10-2026

Activity ID	Activity Name	Original Duration	Schedule % Complete	Performance % Complete	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Variance - BL Project
MLTX-02-005	Playground Initiative for Eastern Region (Arar - Hasa Oasis - Dammam) -R R	186	44.83%	47.47%	16-Apr-26	14-Dec-26	01-Jun-26 A	29-Dec-26	1,135,568.85	1,202,486.22	2,533,327.96	-12
ARAR		108	52.91%	33.43%	27-Jun-26	22-Nov-26	11-Jun-26 A	29-Dec-26	400,103.58	252,810.25	756,158.98	-31
ENGINEERING		27	0%	0%	28-Jun-26	21-Oct-26	20-Oct-26	19-Nov-26	0.00	0.00	0.00	-25
SHOP DRAWINGS		27	0%	0%	28-Jun-26	21-Oct-26	20-Oct-26	19-Nov-26	0.00	0.00	0.00	-25
SHOP DRAWINGS SUBMISSION		27	0%	0%	19-Sep-26	20-Oct-26	20-Oct-26	19-Nov-26	0.00	0.00	0.00	-26
SHOP DRAWINGS SUBMITTALS FOR PLAYGROUND WORKS		27	0%	0%	19-Sep-26	20-Oct-26	20-Oct-26	19-Nov-26	0.00	0.00	0.00	-26
ELECTRICAL WORKS		27	0%	0%	19-Sep-26	20-Oct-26	20-Oct-26	19-Nov-26	0.00	0.00	0.00	-26
MLTX-02-005-EN-2580	Shop DWG Submittal for Power Layout	27	96.3%	0%	19-Sep-26	20-Oct-26	20-Oct-26	19-Nov-26	0.00	0.00	0.00	-26
MLTX-02-005-EN-2610	Shop DWG Submittal for Fire Alarm Layout	15	100%	0%	19-Sep-26	06-Oct-26	20-Oct-26	05-Nov-26	0.00	0.00	0.00	-26
SHOP DRAWINGS APPROVALS		23	0%	0%	28-Jun-26	21-Oct-26	20-Oct-26	15-Nov-26	0.00	0.00	0.00	-21
SHOP DRAWINGS APPROVAL FOR PLAYGROUND WORKS		23	0%	0%	28-Jun-26	21-Oct-26	20-Oct-26	15-Nov-26	0.00	0.00	0.00	-21
AIR DOME SYSTEM		15	0%	0%	28-Jun-26	14-Jul-26	20-Oct-26	05-Nov-26	0.00	0.00	0.00	-97
MLTX-02-005-EN-3560	Shop DWG Approval for Membrane Panel Layout	15	100%	0%	28-Jun-26	14-Jul-26	20-Oct-26	05-Nov-26	0.00	0.00	0.00	-97
MLTX-02-005-EN-3570	Shop DWG Approval for Cable Tension Layout	13	100%	0%	30-Jun-26	14-Jul-26	22-Oct-26	05-Nov-26	0.00	0.00	0.00	-97
ELECTRICAL WORKS		23	0%	0%	26-Sep-26	21-Oct-26	20-Oct-26	15-Nov-26	0.00	0.00	0.00	-21
MLTX-02-005-EN-3680	Shop DWG Approval for Lighting Layout	23	91.3%	0%	26-Sep-26	21-Oct-26	20-Oct-26	15-Nov-26	0.00	0.00	0.00	-21
PROCUREMENT		40	0%	0%	27-Jun-26	24-Oct-26	20-Oct-26	05-Dec-26	0.00	0.00	0.00	-36
SHORT LEAD ITEM		40	0%	0%	27-Jun-26	24-Oct-26	20-Oct-26	05-Dec-26	0.00	0.00	0.00	-36
TOILET/SERVICE WORKS		40	0%	0%	27-Jun-26	10-Oct-26	20-Oct-26	05-Dec-26	0.00	0.00	0.00	-48
LIGHTING FIXTURES		40	0%	0%	27-Jun-26	11-Aug-26	20-Oct-26	05-Dec-26	0.00	0.00	0.00	-98
MLTX-02-005-PR-8490	Material Delivery for Lighting Fixtures	40	100%	0%	27-Jun-26	11-Aug-26	20-Oct-26	05-Dec-26	0.00	0.00	0.00	-98
SWITCHES/SOCKETS		15	0%	0%	22-Sep-26	10-Oct-26	20-Oct-26	05-Nov-26	0.00	0.00	0.00	-23
MLTX-02-005-PR-8510	PO for Switches/Sockets	15	100%	0%	22-Sep-26	10-Oct-26	20-Oct-26	05-Nov-26	0.00	0.00	0.00	-23
DISTRIBUTION PANNELS		5	0%	0%	27-Sep-26	01-Oct-26	20-Oct-26	25-Oct-26	0.00	0.00	0.00	-20
MLTX-02-005-PR-8590	PO for Distribution Panels	5	100%	0%	27-Sep-26	01-Oct-26	20-Oct-26	25-Oct-26	0.00	0.00	0.00	-20
FURNITURES		29	0%	0%	30-Aug-26	03-Oct-26	20-Oct-26	22-Nov-26	0.00	0.00	0.00	-43
MLTX-02-005-PR-8150	PO for Furnitures	29	100%	0%	30-Aug-26	03-Oct-26	20-Oct-26	22-Nov-26	0.00	0.00	0.00	-43
PLAYGROUND WORKS		30	0%	0%	15-Jul-26	24-Oct-26	20-Oct-26	23-Nov-26	0.00	0.00	0.00	-26
PADEL WIRE MESH/STEEL SETS		15	0%	0%	31-Aug-26	16-Sep-26	20-Oct-26	05-Nov-26	0.00	0.00	0.00	-42
MLTX-02-005-PR-8970	Material Delivery for Wire Mesh/Steel Sets	15	100%	0%	31-Aug-26	16-Sep-26	20-Oct-26	05-Nov-26	0.00	0.00	0.00	-42
MARKING PAINT		15	0%	0%	10-Sep-26	28-Sep-26	20-Oct-26	05-Nov-26	0.00	0.00	0.00	-33
MLTX-02-005-PR-9090	PO for Marking Paint	15	100%	0%	10-Sep-26	28-Sep-26	20-Oct-26	05-Nov-26	0.00	0.00	0.00	-33
EXHAUST FANS		20	0%	0%	16-Sep-26	10-Oct-26	20-Oct-26	11-Nov-26	0.00	0.00	0.00	-28
MLTX-02-005-PR-9250	PO for Exhaust Fans	5	100%	0%	16-Sep-26	21-Sep-26	20-Oct-26	25-Oct-26	0.00	0.00	0.00	-28
MLTX-02-005-PR-9270	Material Delivery for Exhaust Fans	15	100%	0%	22-Sep-26	10-Oct-26	26-Oct-26	11-Nov-26	0.00	0.00	0.00	-28
CCTV MATERIALS		25	0%	0%	26-Sep-26	24-Oct-26	20-Oct-26	17-Nov-26	0.00	0.00	0.00	-21
MLTX-02-005-PR-9410	PO for CCTV	25	84%	0%	26-Sep-26	24-Oct-26	20-Oct-26	17-Nov-26	0.00	0.00	0.00	-21
POWER OUTLETS/SWITCHES		30	0%	0%	15-Jul-26	18-Aug-26	20-Oct-26	23-Nov-26	0.00	0.00	0.00	-82
MLTX-02-005-PR-9470	Material Delivery for Power Outlets/Switches	30	100%	0%	15-Jul-26	18-Aug-26	20-Oct-26	23-Nov-26	0.00	0.00	0.00	-82
LANDSCAPE WORKS		20	0%	0%	15-Jul-26	17-Aug-26	20-Oct-26	11-Nov-26	0.00	0.00	0.00	-73
PAVEMENT MARKING		5	0%	0%	15-Jul-26	20-Jul-26	20-Oct-26	25-Oct-26	0.00	0.00	0.00	-82
MLTX-02-005-PR-9580	PO for Pavement Markings	5	100%	0%	15-Jul-26	20-Jul-26	20-Oct-26	25-Oct-26	0.00	0.00	0.00	-82
TRAFFIC SIGNS		15	0%	0%	27-Jul-26	12-Aug-26	26-Oct-26	11-Nov-26	0.00	0.00	0.00	-77
MLTX-02-005-PR-9620	PO for Traffic Signs	15	100%	0%	27-Jul-26	12-Aug-26	26-Oct-26	11-Nov-26	0.00	0.00	0.00	-77
AGRICULTURE SOIL		15	0%	0%	01-Aug-26	17-Aug-26	20-Oct-26	05-Nov-26	0.00	0.00	0.00	-68
MLTX-02-005-PR-9700	PO for Agriculture Soil	15	100%	0%	01-Aug-26	17-Aug-26	20-Oct-26	05-Nov-26	0.00	0.00	0.00	-68
LONG LEAD ITEM		20	0%	0%	08-Sep-26	01-Oct-26	20-Oct-26	11-Nov-26	0.00	0.00	0.00	-35
PLAYGROUND WORKS		20	0%	0%	08-Sep-26	01-Oct-26	20-Oct-26	11-Nov-26	0.00	0.00	0.00	-35
EMERGENCY DOORS		20	0%	0%	08-Sep-26	01-Oct-26	20-Oct-26	11-Nov-26	0.00	0.00	0.00	-35
MLTX-02-005-PR-8710	PO for Emergency Doors	20	100%	0%	08-Sep-26	01-Oct-26	20-Oct-26	11-Nov-26	0.00	0.00	0.00	-35
PRESSURE UNITS		10	0%	0%	08-Sep-26	19-Sep-26	20-Oct-26	31-Oct-26	0.00	0.00	0.00	-35
MLTX-02-005-PR-8750	PO for Pressure Units	10	100%	0%	08-Sep-26	19-Sep-26	20-Oct-26	31-Oct-26	0.00	0.00	0.00	-35
CONSTRUCTION PHASE		108	52.91%	33.43%	31-Aug-26	22-Nov-26	11-Jun-26 A	29-Dec-26	400,103.58	252,810.25	756,158.98	-31
SITE WORKS		90	39.54%	41.2%	01-Oct-26	22-Nov-26	11-Jun-26 A	29-Dec-26	227,102.75	236,638.67	574,383.78	-31
LANDSCAPE WORKS		90	39.54%	41.2%	01-Oct-26	22-Nov-26	11-Jun-26 A	29-Dec-26	227,102.75	236,638.67	574,383.78	-31
PLAYGROUND AREA		20	80%	0%	01-Oct-26	24-Oct-26	20-Oct-26	11-Nov-26	24,541.99	0.00	30,677.48	-16
PADEL FENCE		20	80%	0%	01-Oct-26	24-Oct-26	20-Oct-26	11-Nov-26	24,541.99	0.00	30,677.48	-16
MLTX-02-005-CN-1026(	Tempered Glass Fenc Installation and Fixation	20	80%	0%	01-Oct-26	24-Oct-26	20-Oct-26	11-Nov-26	24,541.99	0.00	30,677.48	-16
WALKING/BIKE PATHS		24	55.1%	50%	05-Oct-26	01-Nov-26	11-Jun-26 A	29-Dec-26	202,560.77	183,816.95	367,633.90	-49
MLTX-02-005-CN-10510	Bike Path Preparation and Installation Works	12	100%	50%	05-Oct-26	18-Oct-26	11-Jun-26 A	29-Dec-26	187,554.12	93,777.06	187,554.12	-61
MLTX-02-005-CN-10520	Walking Path Preparation and Installation Works	12	8.33%	50%	19-Oct-26	01-Nov-26	11-Jun-26 A	29-Dec-26	15,006.65	90,039.89	180,079.78	-49
GENERAL/FURNITURE		13	0%	30%	08-Nov-26	22-Nov-26	18-Oct-26 A	03-Nov-26	0.00	52,821.72	176,072.40	16
MLTX-02-005-CN-11800	Installing of Site Light Poles	13	0%	30%	08-Nov-26	22-Nov-26	18-Oct-26 A	03-Nov-26	0.00	52,821.72	176,072.40	16

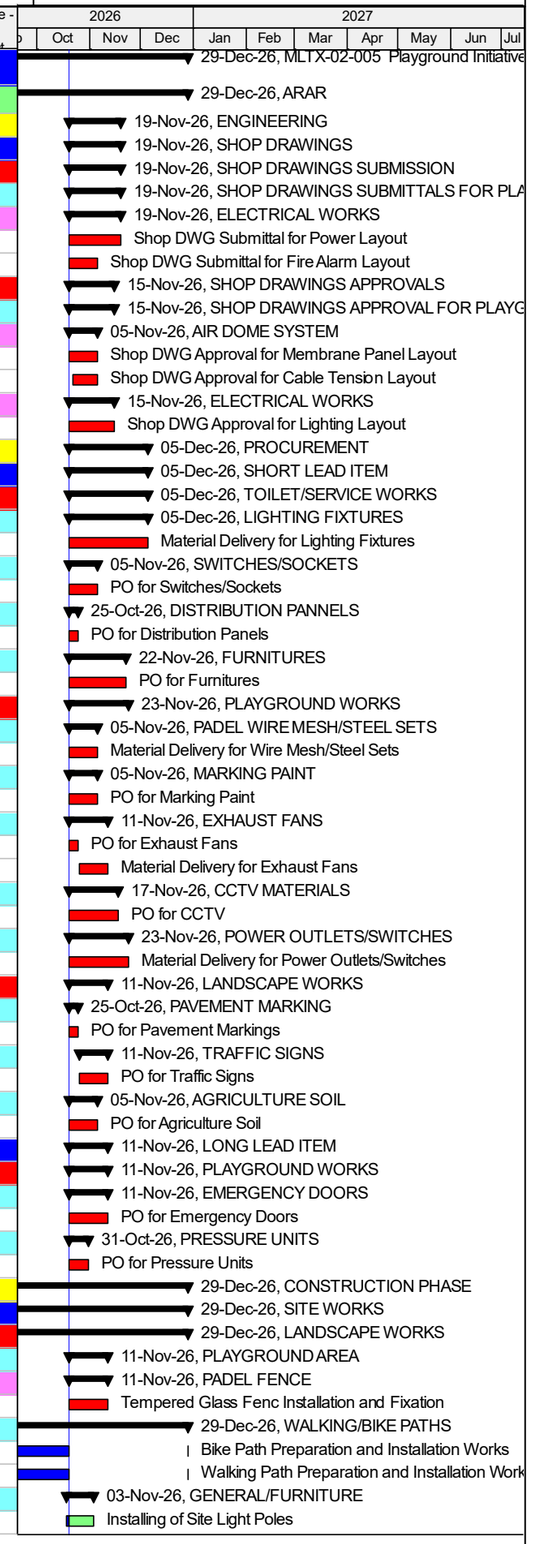

Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary


TASK filter: 2 weeks look ahead .

© Oracle Corporation

MLTX-02-005 - Playground Initiative for Eastern Region (Arar-Hasa osis -Dammam)

2 Weeks look ahead schedule
D.D 19-10-2026

Activity ID	Activity Name	Original Duration	Schedule % Complete	Performance % Complete	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Variance - BL Project
TOILET/SERVICE BUILDING		47	95.17%	8.9%	31-Aug-26	22-Oct-26	03-Oct-26 A	07-Nov-26	173,000.82	16,171.58	181,775.20	-13
THERMAL & MOISTER PROTECTION		37	100%	61.73%	31-Aug-26	21-Sep-26	03-Oct-26 A	28-Oct-26	21,520.94	13,285.82	21,520.94	-31
MLTX-02-005-CN-11070	Finalize Water Proofing Works for Toilets	6	100%	0%	31-Aug-26	06-Sep-26	20-Oct-26	26-Oct-26	4,913.66	0.00	4,913.66	-42
MLTX-02-005-CN-11080	Finalize Water Proofing Works for Roofing and Wet Areas	8	100%	80%	13-Sep-26	21-Sep-26	03-Oct-26 A	28-Oct-26	16,607.28	13,285.82	16,607.28	-31
MECHANICAL WORK		11	100%	0%	29-Sep-26	17-Oct-26	20-Oct-26	01-Nov-26	36,762.98	0.00	36,762.98	-13
SEWER/DRAINAGE SYSTEM		11	100%	0%	29-Sep-26	17-Oct-26	20-Oct-26	01-Nov-26	36,762.98	0.00	36,762.98	-13
MLTX-02-005-CN-11580	Installing UPVC Pipes for External Connection for Sewage Network	4	100%	0%	05-Oct-26	08-Oct-26	26-Oct-26	29-Oct-26	14,217.67	0.00	14,217.67	-18
MLTX-02-005-CN-11600	Installing of Plumping Fixtures and Accessories	2	100%	0%	15-Oct-26	17-Oct-26	31-Oct-26	01-Nov-26	10,358.68	0.00	10,358.68	-13
MLTX-02-005-CN-11850	Installing Inspection Chamber for Sewage Network	5	100%	0%	29-Sep-26	04-Oct-26	20-Oct-26	25-Oct-26	12,186.63	0.00	12,186.63	-18
DOORS/WINDOWS		5	100%	0%	17-Sep-26	22-Sep-26	20-Oct-26	25-Oct-26	60,445.68	0.00	60,445.68	-27
MLTX-02-005-CN-11100	Preliminary Works For Windows/Curtain Wall	2	100%	0%	17-Sep-26	19-Sep-26	20-Oct-26	21-Oct-26	52,646.24	0.00	52,646.24	-27
MLTX-02-005-CN-11110	Preliminary Works For Doors	3	100%	0%	20-Sep-26	22-Sep-26	22-Oct-26	25-Oct-26	7,799.44	0.00	7,799.44	-27
METAL WORKS		4	100%	0%	14-Sep-26	17-Sep-26	20-Oct-26	24-Oct-26	3,899.72	0.00	3,899.72	-30
MLTX-02-005-CN-11160	Installation of DI Cover for Tank	4	100%	0%	14-Sep-26	17-Sep-26	20-Oct-26	24-Oct-26	3,899.72	0.00	3,899.72	-30
FINISHING WORKS		7	100%	6.48%	06-Oct-26	19-Oct-26	19-Oct-26 A	27-Oct-26	44,521.92	2,885.76	44,521.92	-7
FLOOR FINISHES		4	100%	0%	06-Oct-26	10-Oct-26	20-Oct-26	24-Oct-26	2,924.82	0.00	2,924.82	-12
MLTX-02-005-CN-11210	Granite Tiles Floor Finish Works	4	100%	0%	06-Oct-26	10-Oct-26	20-Oct-26	24-Oct-26	2,924.82	0.00	2,924.82	-12
WALL FINISHES		7	100%	0%	06-Oct-26	13-Oct-26	20-Oct-26	27-Oct-26	35,825.58	0.00	35,825.58	-12
MLTX-02-005-CN-11300	Painting Finish Works for External Walls	7	100%	0%	06-Oct-26	13-Oct-26	20-Oct-26	27-Oct-26	35,825.58	0.00	35,825.58	-12
CELLING FINISHES		7	100%	50%	12-Oct-26	19-Oct-26	19-Oct-26 A	27-Oct-26	5,771.52	2,885.76	5,771.52	-7
MLTX-02-005-CN-11360	Gypsum Board Suspended Ceiling Finish Works For Ceiling	7	100%	50%	12-Oct-26	19-Oct-26	19-Oct-26 A	27-Oct-26	5,771.52	2,885.76	5,771.52	-7
SPECIALTIES WORK		5	40%	0%	18-Oct-26	22-Oct-26	02-Nov-26	07-Nov-26	5,849.58	0.00	14,623.96	-13
MLTX-02-005-CN-11390	Sanitary Fixtures and Accessories Works	5	40%	0%	18-Oct-26	22-Oct-26	02-Nov-26	07-Nov-26	5,849.58	0.00	14,623.96	-13
HASA OASIS		186	42.87%	58.43%	04-May-26	07-Dec-26	01-Jun-26 A	23-Nov-26	619,061.51	843,797.67	1,444,068.86	12
ENGINEERING		25	0%	0%	04-May-26	02-Nov-26	20-Oct-26	17-Nov-26	0.00	0.00	0.00	-13
SHOP DRAWINGS		25	0%	0%	04-May-26	02-Nov-26	20-Oct-26	17-Nov-26	0.00	0.00	0.00	-13
SHOP DRAWINGS SUBMISSION		25	0%	0%	04-May-26	27-Oct-26	20-Oct-26	17-Nov-26	0.00	0.00	0.00	-18
SHOP DRAWINGS SUBMITTALS FOR PLAYGROUND WORKS		25	0%	0%	04-May-26	27-Oct-26	20-Oct-26	17-Nov-26	0.00	0.00	0.00	-18
MECHANICAL WORKS		25	0%	0%	26-Sep-26	24-Oct-26	20-Oct-26	17-Nov-26	0.00	0.00	0.00	-21
MLTX-02-005-EN-8760	Shop DWG Submittal for HVAC Plan	25	84%	0%	26-Sep-26	24-Oct-26	20-Oct-26	17-Nov-26	0.00	0.00	0.00	-21
MLTX-02-005-EN-8770	Shop DWG Submittal for Exhaust Air Plan	25	84%	0%	26-Sep-26	24-Oct-26	20-Oct-26	17-Nov-26	0.00	0.00	0.00	-21
ELECTRICAL WORKS		25	0%	0%	04-May-26	27-Oct-26	20-Oct-26	17-Nov-26	0.00	0.00	0.00	-18
MLTX-02-005-EN-8650	Shop DWG Submittal for Lighting Layout	25	84%	0%	26-Sep-26	24-Oct-26	20-Oct-26	17-Nov-26	0.00	0.00	0.00	-21
MLTX-02-005-EN-8660	Shop DWG Submittal for Power Layout	25	100%	0%	04-May-26	04-Jun-26	20-Oct-26	17-Nov-26	0.00	0.00	0.00	-141
MLTX-02-005-EN-8670	Shop DWG Submittal for Power Single Line Diagram	25	72%	0%	29-Sep-26	27-Oct-26	20-Oct-26	17-Nov-26	0.00	0.00	0.00	-18
MLTX-02-005-EN-8680	Shop DWG Submittal for Panel Board Schedules	25	72%	0%	29-Sep-26	27-Oct-26	20-Oct-26	17-Nov-26	0.00	0.00	0.00	-18
MLTX-02-005-EN-8690	Shop DWG Submittal for Power Installation Details	25	72%	0%	29-Sep-26	27-Oct-26	20-Oct-26	17-Nov-26	0.00	0.00	0.00	-18
SHOP DRAWINGS APPROVALS		21	0%	0%	10-Oct-26	02-Nov-26	20-Oct-26	12-Nov-26	0.00	0.00	0.00	-9
SHOP DRAWINGS APPROVAL FOR PLAYGROUND WORKS		21	0%	0%	10-Oct-26	02-Nov-26	20-Oct-26	12-Nov-26	0.00	0.00	0.00	-9
SPORTS EQUIPMENT		21	0%	0%	10-Oct-26	02-Nov-26	20-Oct-26	12-Nov-26	0.00	0.00	0.00	-9
MLTX-02-005-EN-1207(	Shop DWG Approval for Football Turf Installation	21	42.86%	0%	10-Oct-26	02-Nov-26	20-Oct-26	12-Nov-26	0.00	0.00	0.00	-9
PROCUREMENT		30	0%	0%	10-Jun-26	03-Nov-26	20-Oct-26	23-Nov-26	0.00	0.00	0.00	-17
SHORT LEAD ITEM		30	0%	0%	16-Jun-26	03-Nov-26	20-Oct-26	23-Nov-26	0.00	0.00	0.00	-17
TOILET/SERVICE WORKS		20	0%	0%	16-Jun-26	19-Oct-26	20-Oct-26	11-Nov-26	0.00	0.00	0.00	-20
LIGHTING FIXTURES		20	0%	0%	16-Jun-26	08-Jul-26	20-Oct-26	11-Nov-26	0.00	0.00	0.00	-107
MLTX-02-005-PR-10300	Material Delivery for Lighting Fixtures	20	100%	0%	16-Jun-26	08-Jul-26	20-Oct-26	11-Nov-26	0.00	0.00	0.00	-107
SWITCHES/SOCKETS		15	0%	0%	16-Jun-26	02-Jul-26	20-Oct-26	05-Nov-26	0.00	0.00	0.00	-107
MLTX-02-005-PR-10310	PO for Switches/Sockets	15	100%	0%	16-Jun-26	02-Jul-26	20-Oct-26	05-Nov-26	0.00	0.00	0.00	-107
DISTRIBUTION PANNELS		20	0%	0%	27-Sep-26	19-Oct-26	20-Oct-26	11-Nov-26	0.00	0.00	0.00	-20
MLTX-02-005-PR-10130	PO for Distribution Panels	5	100%	0%	27-Sep-26	01-Oct-26	20-Oct-26	25-Oct-26	0.00	0.00	0.00	-20
MLTX-02-005-PR-10140	Material Delivery for Distribution Panels	15	100%	0%	03-Oct-26	19-Oct-26	26-Oct-26	11-Nov-26	0.00	0.00	0.00	-20
FURNITURES		19	0%	0%	16-Jun-26	07-Jul-26	20-Oct-26	10-Nov-26	0.00	0.00	0.00	-107
MLTX-02-005-PR-10330	PO for Furnitures	19	100%	0%	16-Jun-26	07-Jul-26	20-Oct-26	10-Nov-26	0.00	0.00	0.00	-107
PLAYGROUND WORKS		30	0%	0%	28-Jun-26	03-Nov-26	20-Oct-26	23-Nov-26	0.00	0.00	0.00	-17
ARTIFICIAL TURF		30	0%	0%	30-Sep-26	03-Nov-26	20-Oct-26	23-Nov-26	0.00	0.00	0.00	-17
MLTX-02-005-PR-10780	Material Delivery for Artificial TURF	30	56.67%	0%	30-Sep-26	03-Nov-26	20-Oct-26	23-Nov-26	0.00	0.00	0.00	-17
RUBBER GRANULES		30	0%	0%	20-Sep-26	25-Oct-26	20-Oct-26	23-Nov-26	0.00	0.00	0.00	-25
MLTX-02-005-PR-10800	Material Delivery for Rubber Granules	30	83.33%	0%	20-Sep-26	25-Oct-26	20-Oct-26	23-Nov-26	0.00	0.00	0.00	-25
PADEL GLASS		30	0%	0%	16-Sep-26	21-Oct-26	20-Oct-26	23-Nov-26	0.00	0.00	0.00	-28
MLTX-02-005-PR-10820	Material Delivery for Padel Glass	30	93.33%	0%	16-Sep-26	21-Oct-26	20-Oct-26	23-Nov-26	0.00	0.00	0.00	-28
PADEL WIRE MESH/STEEL SETS		15	0%	0%	16-Sep-26	04-Oct-26	20-Oct-26	05-Nov-26	0.00	0.00	0.00	-28
MLTX-02-005-PR-10840	Material Delivery for Wire Mesh/Steel Sets	15	100%	0%	16-Sep-26	04-Oct-26	20-Oct-26	05-Nov-26	0.00	0.00	0.00	-28
MARKING PAINT		15	0%	0%	28-Jun-26	14-Jul-26	20-Oct-26	05-Nov-26	0.00	0.00	0.00	-97
MLTX-02-005-PR-10350	PO for Marking Paint	15	100%	0%	28-Jun-26	14-Jul-26	20-Oct-26	05-Nov-26	0.00	0.00	0.00	-97

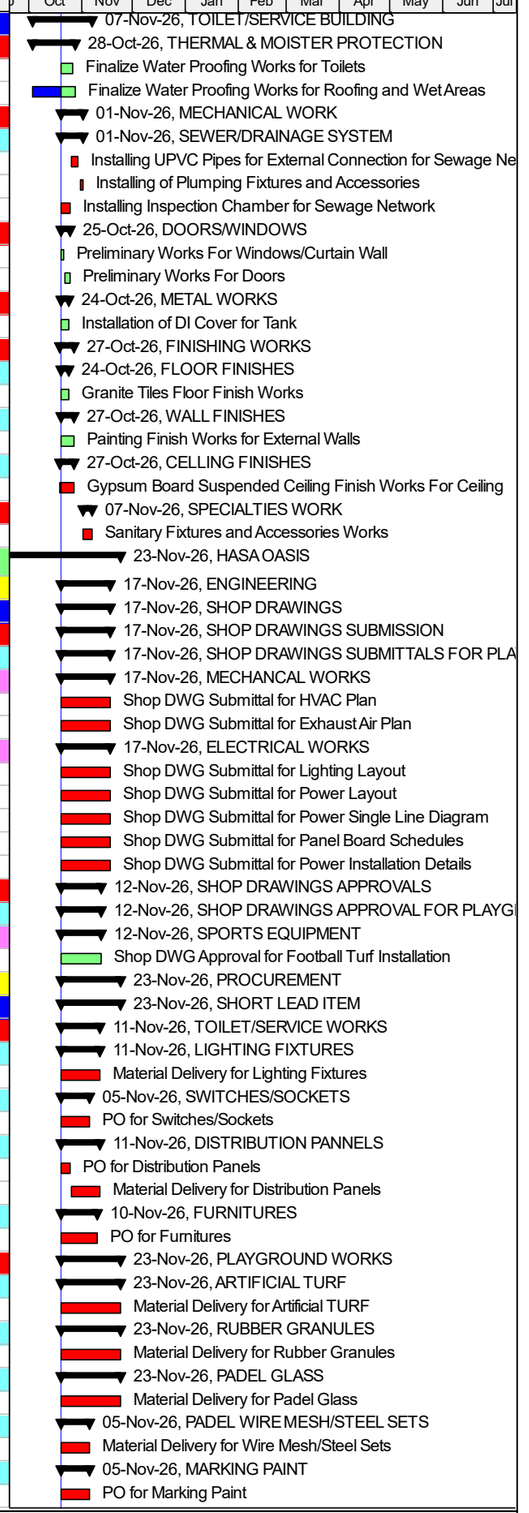

Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary


TASK filter: 2 weeks look ahead .

© Oracle Corporation

MLTX-02-005 - Playground Initiative for Eastern Region (Arar-Hasa osis -Dammam)

2 Weeks look ahead schedule
D.D 19-10-2026

Activity ID	Activity Name	Original Duration	Schedule % Complete	Performance % Complete	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Variance - BL Project
AIR DIFUSSERS/GRILLS		15	0%	0%	24-Sep-26	11-Oct-26	20-Oct-26	05-Nov-26	0.00	0.00	0.00	-22
MLTX-02-005-PR-10470	PO for Air Difussers/Grills	15	100%	0%	24-Sep-26	11-Oct-26	20-Oct-26	05-Nov-26	0.00	0.00	0.00	-22
GALVANIZED DUCTS		15	0%	0%	24-Sep-26	11-Oct-26	20-Oct-26	05-Nov-26	0.00	0.00	0.00	-22
MLTX-02-005-PR-10490	PO for Galvanized Duct	15	100%	0%	24-Sep-26	11-Oct-26	20-Oct-26	05-Nov-26	0.00	0.00	0.00	-22
EXHAUST FANS		15	0%	0%	10-Sep-26	28-Sep-26	20-Oct-26	05-Nov-26	0.00	0.00	0.00	-33
MLTX-02-005-PR-10510	PO for Exhaust Fans	15	100%	0%	10-Sep-26	28-Sep-26	20-Oct-26	05-Nov-26	0.00	0.00	0.00	-33
CCTV MATERIALS		15	0%	0%	04-Jul-26	20-Jul-26	20-Oct-26	05-Nov-26	0.00	0.00	0.00	-92
MLTX-02-005-PR-10690	PO for CCTV	15	100%	0%	04-Jul-26	20-Jul-26	20-Oct-26	05-Nov-26	0.00	0.00	0.00	-92
LONG LEAD ITEM		30	0%	0%	10-Jun-26	14-Jul-26	20-Oct-26	23-Nov-26	0.00	0.00	0.00	-112
PLAYGROUND WORKS		30	0%	0%	10-Jun-26	14-Jul-26	20-Oct-26	23-Nov-26	0.00	0.00	0.00	-112
EMERGENCY DOORS		30	0%	0%	10-Jun-26	14-Jul-26	20-Oct-26	23-Nov-26	0.00	0.00	0.00	-112
MLTX-02-005-PR-10570	PO for Emergency Doors	10	100%	0%	10-Jun-26	21-Jun-26	20-Oct-26	31-Oct-26	0.00	0.00	0.00	-112
MLTX-02-005-PR-10940	Material Fabrication for Emergency Doors	20	100%	0%	22-Jun-26	14-Jul-26	01-Nov-26	23-Nov-26	0.00	0.00	0.00	-112
CONSTRUCTION PHASE		186	42.87%	58.43%	30-Jul-26	07-Dec-26	01-Jun-26 A	21-Nov-26	619,061.51	843,797.67	1,444,068.86	14
SITE WORKS		135	40.83%	57.12%	29-Sep-26	07-Dec-26	01-Jun-26 A	21-Nov-26	561,021.73	784,908.93	1,374,087.22	14
LANDSCAPE WORKS		135	40.83%	57.12%	29-Sep-26	07-Dec-26	01-Jun-26 A	21-Nov-26	561,021.73	784,908.93	1,374,087.22	14
PLAYGROUND AREA		3	100%	70%	29-Sep-26	01-Oct-26	21-Sep-26 A	22-Oct-26	180,520.67	126,364.47	180,520.67	-18
CURBSTOEN/INTERLOCK		3	100%	70%	29-Sep-26	01-Oct-26	21-Sep-26 A	22-Oct-26	180,520.67	126,364.47	180,520.67	-18
MLTX-02-005-CN-1196(	Interlock Installation (Grey Scale) for LandScape (Including Finishing Works)	3	100%	70%	29-Sep-26	01-Oct-26	21-Sep-26 A	22-Oct-26	180,520.67	126,364.47	180,520.67	-18
NATURAL GROUND		15	0%	53.56%	29-Nov-26	07-Dec-26	13-Oct-26 A	25-Oct-26	0.00	102,696.00	191,740.00	37
MLTX-02-005-CN-11980	Tartan Floor Installation Works for Landscape (Including Finishing Works)	3	0%	40%	05-Dec-26	07-Dec-26	14-Oct-26 A	22-Oct-26	0.00	50,696.00	126,740.00	39
MLTX-02-005-CN-11990	Compacted Natural Ground Soil Installation Works for Landscape	5	0%	80%	29-Nov-26	03-Dec-26	13-Oct-26 A	25-Oct-26	0.00	52,000.00	65,000.00	34
PLANTING		101	0%	42%	24-Oct-26	02-Nov-26	03-Oct-26 A	22-Oct-26	0.00	145,845.61	347,251.46	9
MLTX-02-005-CN-12050	Placement of Sweet/Agricultural Soil (Including Levelling and Grading)	3	0%	70%	24-Oct-26	26-Oct-26	03-Oct-26 A	22-Oct-26	0.00	72,922.81	104,175.44	3
MLTX-02-005-CN-12060	Placement of Lawn Ground Cover (Rolling and Compaction)	3	0%	30%	31-Oct-26	02-Nov-26	14-Oct-26 A	22-Oct-26	0.00	42,519.75	141,732.50	9
MLTX-02-005-CN-12070	Placement and Fixation of Trees	3	0%	30%	27-Oct-26	29-Oct-26	14-Oct-26 A	22-Oct-26	0.00	30,403.06	101,343.52	6
WALKING/BIKE PATHS		16	100%	75%	29-Sep-26	17-Oct-26	01-Jun-26 A	20-Oct-26	367,633.90	275,725.43	367,633.90	-2
MLTX-02-005-CN-12000	Bike Path Preparation and Installation Works	8	100%	75%	29-Sep-26	07-Oct-26	01-Jun-26 A	20-Oct-26	187,554.12	140,665.59	187,554.12	-10
MLTX-02-005-CN-12010	Walking Path Preparation and Installation Works	8	100%	75%	08-Oct-26	17-Oct-26	10-Jun-26 A	20-Oct-26	180,079.78	135,059.83	180,079.78	-2
GENERAL/FURNITURE		41	4.48%	46.8%	15-Oct-26	02-Dec-26	01-Oct-26 A	21-Nov-26	12,867.16	134,277.42	286,941.19	10
MLTX-02-005-CN-11970	Stamped Concrete Works for LandScape (Including Finishing Works)	18	11.11%	40%	18-Oct-26	07-Nov-26	14-Oct-26 A	09-Nov-26	10,399.33	37,437.60	93,594.00	-2
MLTX-02-005-CN-12440	Fixation and Installation of Steel Frame for Benches	28	14.29%	0%	15-Oct-26	16-Nov-26	20-Oct-26	21-Nov-26	2,467.83	0.00	17,274.79	-4
MLTX-02-005-CN-12930	Installing of Site Light Poles	22	0%	55%	08-Nov-26	02-Dec-26	01-Oct-26 A	14-Nov-26	0.00	96,839.82	176,072.40	16
TOILET/SERVICE BUILDING		75	82.94%	84.15%	30-Jul-26	20-Oct-26	20-Sep-26 A	09-Nov-26	58,039.78	58,888.74	69,981.64	-17
THERMAL & MOISTER PROTECTION		18	100%	90%	30-Jul-26	19-Aug-26	20-Sep-26 A	09-Nov-26	16,607.28	14,946.55	16,607.28	-69
MLTX-02-005-CN-12650	Finalize Water Proofing Works for Roofing and Wet Areas	18	100%	90%	30-Jul-26	19-Aug-26	20-Sep-26 A	09-Nov-26	16,607.28	14,946.55	16,607.28	-69
FINISHING WORKS		8	69.18%	83.21%	27-Sep-26	20-Oct-26	27-Sep-26 A	26-Oct-26	26,808.54	32,243.02	38,750.40	-5
FLOOR FINISHES		6	100%	0%	27-Sep-26	03-Oct-26	20-Oct-26	26-Oct-26	2,924.82	0.00	2,924.82	-20
MLTX-02-005-CN-13050	Granite Tiles Floor Finish Works	6	100%	0%	27-Sep-26	03-Oct-26	20-Oct-26	26-Oct-26	2,924.82	0.00	2,924.82	-20
WALL FINISHES		3	66.67%	90%	18-Oct-26	20-Oct-26	27-Sep-26 A	22-Oct-26	23,883.72	32,243.02	35,825.58	-2
MLTX-02-005-CN-13010	Painting Finish Works for External Walls	3	66.67%	90%	18-Oct-26	20-Oct-26	27-Sep-26 A	22-Oct-26	23,883.72	32,243.02	35,825.58	-2
SPECIALTIES WORK		3	100%	80%	27-Sep-26	29-Sep-26	04-Oct-26 A	22-Oct-26	14,623.96	11,699.17	14,623.96	-20
MLTX-02-005-CN-12700	Sanitary Fixtures and Accessories Works	3	100%	80%	27-Sep-26	29-Sep-26	04-Oct-26 A	22-Oct-26	14,623.96	11,699.17	14,623.96	-20
DAMMAM		131	34.95%	31.79%	16-Apr-26	14-Dec-26	06-Sep-26 A	14-Dec-26	116,403.76	105,878.30	333,100.12	0
ENGINEERING		30	0%	0%	16-Apr-26	01-Jul-26	20-Oct-26	23-Nov-26	0.00	0.00	0.00	-123
SHOP DRAWINGS		30	0%	0%	16-Apr-26	01-Jul-26	20-Oct-26	23-Nov-26	0.00	0.00	0.00	-123
SHOP DRAWINGS SUBMISSION		30	0%	0%	16-Apr-26	01-Jul-26	20-Oct-26	23-Nov-26	0.00	0.00	0.00	-123
SHOP DRAWINGS SUBMITTALS FOR PLAYGROUND WORKS		30	0%	0%	16-Apr-26	01-Jul-26	20-Oct-26	23-Nov-26	0.00	0.00	0.00	-123
AIR DOME SYSTEM		30	0%	0%	16-Apr-26	07-Jun-26	20-Oct-26	23-Nov-26	0.00	0.00	0.00	-144
MLTX-02-005-EN-1316(	Shop DWG Submittal for Cable Tension Layout	15	100%	0%	16-Apr-26	03-May-26	20-Oct-26	05-Nov-26	0.00	0.00	0.00	-156
MLTX-02-005-EN-1317(	Shop DWG Submittal for Airlock Door Details	25	100%	0%	30-Apr-26	01-Jun-26	20-Oct-26	17-Nov-26	0.00	0.00	0.00	-144
MLTX-02-005-EN-1318(	Shop DWG Submittal for Emergency Exit Details	30	100%	0%	30-Apr-26	07-Jun-26	20-Oct-26	23-Nov-26	0.00	0.00	0.00	-144
MECHANCAL WORKS		15	0%	0%	30-Apr-26	14-Jun-26	20-Oct-26	05-Nov-26	0.00	0.00	0.00	-123
MLTX-02-005-EN-1303(	Shop DWG Submittal for HVAC Plan	15	100%	0%	30-Apr-26	17-May-26	20-Oct-26	05-Nov-26	0.00	0.00	0.00	-144
MLTX-02-005-EN-1304(	Shop DWG Submittal for Exhaust Air Plan	15	100%	0%	25-May-26	14-Jun-26	20-Oct-26	05-Nov-26	0.00	0.00	0.00	-123
ELECTRICAL WORKS		30	0%	0%	25-May-26	01-Jul-26	20-Oct-26	23-Nov-26	0.00	0.00	0.00	-123
MLTX-02-005-EN-1293(	Shop DWG Submittal for Power Layout	25	100%	0%	25-May-26	25-Jun-26	20-Oct-26	17-Nov-26	0.00	0.00	0.00	-123
MLTX-02-005-EN-1294(	Shop DWG Submittal for Power Single Line Diagram	25	100%	0%	25-May-26	25-Jun-26	20-Oct-26	17-Nov-26	0.00	0.00	0.00	-123
MLTX-02-005-EN-1295(	Shop DWG Submittal for Panel Board Schedules	25	100%	0%	25-May-26	25-Jun-26	20-Oct-26	17-Nov-26	0.00	0.00	0.00	-123
MLTX-02-005-EN-1296(	Shop DWG Submittal for Power Installation Details	30	100%	0%	25-May-26	01-Jul-26	20-Oct-26	23-Nov-26	0.00	0.00	0.00	-123
SHOP DRAWINGS APPROVALS		30	0%	0%	30-Apr-26	01-Jul-26	20-Oct-26	23-Nov-26	0.00	0.00	0.00	-123
SHOP DRAWINGS APPROVAL FOR PLAYGROUND WORKS		30	0%	0%	30-Apr-26	01-Jul-26	20-Oct-26	23-Nov-26	0.00	0.00	0.00	-123
AIR DOME SYSTEM		15	0%	0%	30-Apr-26	17-May-26	20-Oct-26	05-Nov-26	0.00	0.00	0.00	-144
MLTX-02-005-EN-1627(	Shop DWG Approval for Air Dome Structural Layout	15	100%	0%	30-Apr-26	17-May-26	20-Oct-26	05-Nov-26	0.00	0.00	0.00	-144

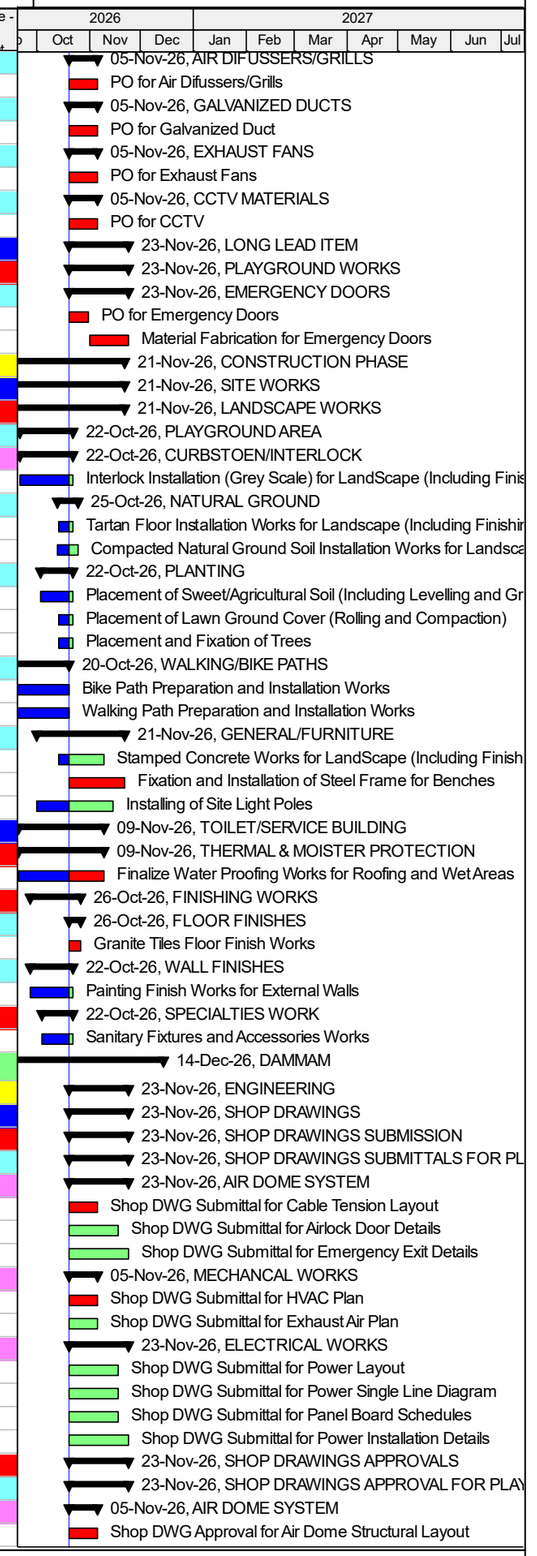

Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary


TASK filter: 2 weeks look ahead .

© Oracle Corporation

MLTX-02-005 - Playground Initiative for Eastern Region (Arar-Hasa osis -Dammam)

2 Weeks look ahead schedule
D.D 19-10-2026

Activity ID	Activity Name	Original Duration	Schedule % Complete	Performance % Complete	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Variance - BL Project
SPORTS EQUIPMENT		30	0%	0%	25-May-26	01-Jul-26	20-Oct-26	23-Nov-26	0.00	0.00	0.00	-123
MLTX-02-005-EN-1634(	Shop DWG Approval for Football Turf Installation	30	100%	0%	25-May-26	01-Jul-26	20-Oct-26	23-Nov-26	0.00	0.00	0.00	-123
PROCUREMENT		29	0%	0%	21-May-26	29-Oct-26	20-Oct-26	22-Nov-26	0.00	0.00	0.00	-20
SHORT LEAD ITEM		29	0%	0%	21-May-26	29-Oct-26	20-Oct-26	22-Nov-26	0.00	0.00	0.00	-20
TOILET/SERVICE WORKS		29	0%	0%	17-Jun-26	29-Oct-26	20-Oct-26	22-Nov-26	0.00	0.00	0.00	-20
DISTRIBUTION PANNELS		15	0%	0%	13-Oct-26	29-Oct-26	20-Oct-26	05-Nov-26	0.00	0.00	0.00	-6
MLTX-02-005-PR-11210	PO for Distribution Panels	15	40%	0%	13-Oct-26	29-Oct-26	20-Oct-26	05-Nov-26	0.00	0.00	0.00	-6
FURNITURES		29	0%	0%	17-Jun-26	20-Jul-26	20-Oct-26	22-Nov-26	0.00	0.00	0.00	-106
MLTX-02-005-PR-11410	PO for Furnitures	9	100%	0%	17-Jun-26	27-Jun-26	20-Oct-26	29-Oct-26	0.00	0.00	0.00	-106
MLTX-02-005-PR-11420	Material Delivery for Furnitures	20	100%	0%	28-Jun-26	20-Jul-26	31-Oct-26	22-Nov-26	0.00	0.00	0.00	-106
PLAYGROUND WORKS		21	0%	0%	21-May-26	18-Oct-26	20-Oct-26	12-Nov-26	0.00	0.00	0.00	-22
PVC MEMBRANE		21	0%	0%	21-May-26	17-Jun-26	20-Oct-26	12-Nov-26	0.00	0.00	0.00	-126
MLTX-02-005-PR-11620	Material Delivery for PVC Membrane	21	100%	0%	21-May-26	17-Jun-26	20-Oct-26	12-Nov-26	0.00	0.00	0.00	-126
RUBBER GRANULES		12	0%	0%	31-May-26	13-Jun-26	20-Oct-26	02-Nov-26	0.00	0.00	0.00	-121
MLTX-02-005-PR-11880	Material Delivery for Rubber Granules	12	100%	0%	31-May-26	13-Jun-26	20-Oct-26	02-Nov-26	0.00	0.00	0.00	-121
PADEL WIRE MESH/STEEL SETS		15	0%	0%	06-Jun-26	22-Jun-26	20-Oct-26	05-Nov-26	0.00	0.00	0.00	-116
MLTX-02-005-PR-11920	Material Delivery for Wire Mesh/Steel Sets	15	100%	0%	06-Jun-26	22-Jun-26	20-Oct-26	05-Nov-26	0.00	0.00	0.00	-116
AIR DIFUSSERS/GRILLS		15	0%	0%	01-Oct-26	18-Oct-26	20-Oct-26	05-Nov-26	0.00	0.00	0.00	-16
MLTX-02-005-PR-11550	PO for Air Difussers/Grills	15	100%	0%	01-Oct-26	18-Oct-26	20-Oct-26	05-Nov-26	0.00	0.00	0.00	-16
EXHAUST FANS		15	0%	0%	17-Jun-26	04-Jul-26	20-Oct-26	05-Nov-26	0.00	0.00	0.00	-106
MLTX-02-005-PR-11590	PO for Exhaust Fans	15	100%	0%	17-Jun-26	04-Jul-26	20-Oct-26	05-Nov-26	0.00	0.00	0.00	-106
CCTV MATERIALS		5	0%	0%	30-Jul-26	04-Aug-26	20-Oct-26	25-Oct-26	0.00	0.00	0.00	-69
MLTX-02-005-PR-11770	PO for CCTV	5	100%	0%	30-Jul-26	04-Aug-26	20-Oct-26	25-Oct-26	0.00	0.00	0.00	-69
LANDSCAPE WORKS		15	0%	0%	05-Aug-26	22-Aug-26	20-Oct-26	05-Nov-26	0.00	0.00	0.00	-64
AGRICULTURE SOIL		15	0%	0%	05-Aug-26	22-Aug-26	20-Oct-26	05-Nov-26	0.00	0.00	0.00	-64
MLTX-02-005-PR-11930	PO for Agriculture Soil	15	100%	0%	05-Aug-26	22-Aug-26	20-Oct-26	05-Nov-26	0.00	0.00	0.00	-64
LONG LEAD ITEM		18	0%	0%	21-May-26	14-Jun-26	20-Oct-26	09-Nov-26	0.00	0.00	0.00	-126
PLAYGROUND WORKS		18	0%	0%	21-May-26	14-Jun-26	20-Oct-26	09-Nov-26	0.00	0.00	0.00	-126
STEEL TENSION CABLES		18	0%	0%	21-May-26	14-Jun-26	20-Oct-26	09-Nov-26	0.00	0.00	0.00	-126
MLTX-02-005-PR-11630	PO for Steel Tension Cables	8	100%	0%	21-May-26	02-Jun-26	20-Oct-26	28-Oct-26	0.00	0.00	0.00	-126
MLTX-02-005-PR-12010	Material Fabrication for Steel Tension Cables	10	100%	0%	03-Jun-26	14-Jun-26	29-Oct-26	09-Nov-26	0.00	0.00	0.00	-126
CONSTRUCTION PHASE		131	34.95%	31.79%	18-Aug-26	14-Dec-26	06-Sep-26 A	14-Dec-26	116,403.76	105,878.30	333,100.12	0
SITE WORKS		78	16.18%	32.87%	10-Oct-26	14-Dec-26	15-Oct-26 A	11-Nov-26	39,000.00	79,232.58	241,072.40	28
LANDSCAPE WORKS		78	16.18%	32.87%	10-Oct-26	14-Dec-26	15-Oct-26 A	11-Nov-26	39,000.00	79,232.58	241,072.40	28
NATURAL GROUND		15	60%	0%	10-Oct-26	26-Oct-26	20-Oct-26	05-Nov-26	39,000.00	0.00	65,000.00	-9
MLTX-02-005-CN-13420	Compacted Natural Ground Soil Installation Works for Landscape	15	60%	0%	10-Oct-26	26-Oct-26	20-Oct-26	05-Nov-26	39,000.00	0.00	65,000.00	-9
GENERAL/FURNITURE		20	0%	45%	22-Nov-26	14-Dec-26	15-Oct-26 A	11-Nov-26	0.00	79,232.58	176,072.40	28
MLTX-02-005-CN-14360	Installing of Site Light Poles	20	0%	45%	22-Nov-26	14-Dec-26	15-Oct-26 A	11-Nov-26	0.00	79,232.58	176,072.40	28
TOILET/SERVICE BUILDING		130	84.11%	28.95%	18-Aug-26	31-Oct-26	06-Sep-26 A	14-Dec-26	77,403.76	26,645.72	92,027.72	-38
THERMAL & MOISTER PROTECTION		8	100%	90%	18-Aug-26	26-Aug-26	06-Sep-26 A	28-Oct-26	16,607.28	14,946.55	16,607.28	-53
MLTX-02-005-CN-14080	Finalize Water Proofing Works for Roofing and Wet Areas	8	100%	90%	18-Aug-26	26-Aug-26	06-Sep-26 A	28-Oct-26	16,607.28	14,946.55	16,607.28	-53
DOORS/WINDOWS		12	100%	0%	19-Sep-26	03-Oct-26	20-Oct-26	02-Nov-26	52,646.24	0.00	52,646.24	-26
MLTX-02-005-CN-14550	Preliminary Works For Windows/Curtain Wall	12	100%	0%	19-Sep-26	03-Oct-26	20-Oct-26	02-Nov-26	52,646.24	0.00	52,646.24	-26
FINISHING WORKS		12	100%	0%	27-Aug-26	09-Sep-26	29-Oct-26	11-Nov-26	8,150.24	0.00	8,150.24	-53
WALL FINISHES		12	100%	0%	27-Aug-26	09-Sep-26	29-Oct-26	11-Nov-26	8,150.24	0.00	8,150.24	-53
MLTX-02-005-CN-14580	Granite Capping for Parpet	12	100%	0%	27-Aug-26	09-Sep-26	29-Oct-26	11-Nov-26	8,150.24	0.00	8,150.24	-53
SPECIALTIES WORK		4	0%	80%	27-Oct-26	31-Oct-26	12-Oct-26 A	14-Dec-26	0.00	11,699.17	14,623.96	-38
MLTX-02-005-CN-14130	Sanitary Fixtures and Accessories Works	4	0%	80%	27-Oct-26	31-Oct-26	12-Oct-26 A	14-Dec-26	0.00	11,699.17	14,623.96	-38

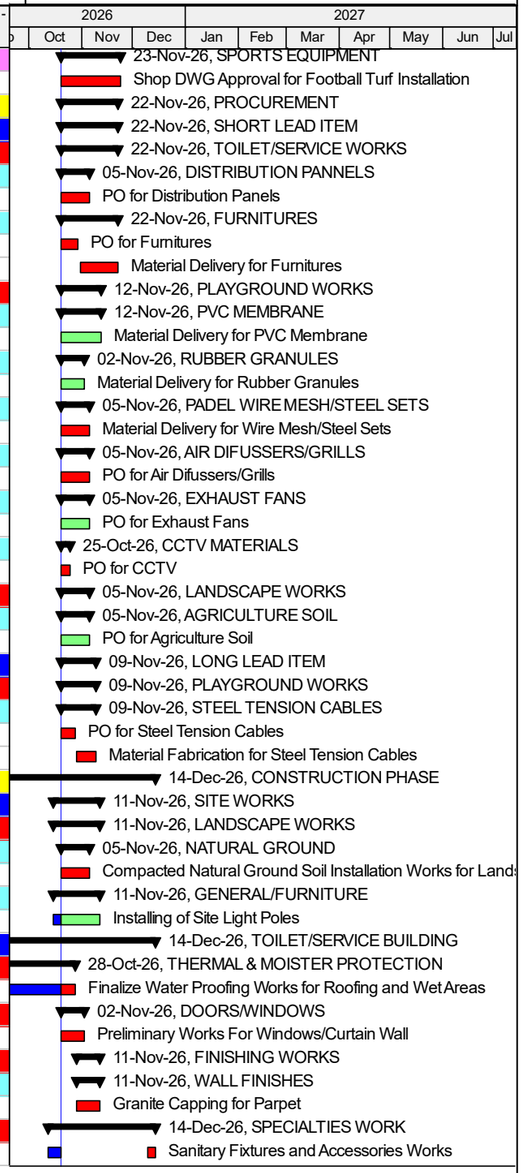

Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary

TASK filter: 2 weeks look ahead .

© Oracle Corporation
