
MLTX-02-005 - Playground Initiative for Eastern Region (Arar-Hasa osis -Dammam)

WBS Summary
D.D 19-10-2026

Activity ID	Activity Name	Original Duration	Schedule % Complete	Performance % Complete	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Variance - BL Project
MLTX-02-005	Playground Initiative for Eastern Region (Arar - Hasa Oa	344	38.2%	38.51%	03-Mar-26	02-Jan-27	03-Mar-26 A	20-Apr-27	11,460,225.95	11,553,630.65	29,997,851.67	-89
KEY MILESTONES		344	0%	0%	03-Mar-26	02-Jan-27	03-Mar-26 A	20-Apr-27	0.00	0.00	0.00	-89
GENERAL MILESTONES		344	0%	0%	03-Mar-26	02-Jan-27	03-Mar-26 A	20-Apr-27	0.00	0.00	0.00	-89
CONTRACTUAL MILESTONE		312	0%	0%	11-Apr-26	02-Jan-27	02-Apr-26 A	19-Apr-27	0.00	0.00	0.00	-88
ARAR		318	36.59%	34.97%	03-Mar-26	02-Jan-27	04-Mar-26 A	21-Mar-27	3,742,315.66	3,575,773.78	10,226,640.03	-63
MOBILIZATION		34	0%	0%	03-Mar-26	14-Apr-26	04-Mar-26 A	04-Apr-26 A	0.00	0.00	0.00	9
ENGINEERING		256	0%	0%	07-Mar-26	13-Dec-26	07-Mar-26 A	06-Jan-27	0.00	0.00	0.00	-21
PROCUREMENT		220	0%	0%	09-Jun-26	15-Dec-26	02-Apr-26 A	21-Feb-27	0.00	0.00	0.00	-58
CONSTRUCTION PHASE		284	36.59%	34.97%	15-Apr-26	31-Dec-26	04-Apr-26 A	21-Mar-27	3,742,315.66	3,575,773.78	10,226,640.03	-64
SITE WORKS		284	32.96%	32.85%	15-Apr-26	30-Dec-26	04-Apr-26 A	21-Mar-27	2,985,491.60	2,975,778.97	9,058,565.25	-65
EARTH WORKS		68	100%	100%	15-Apr-26	06-Jul-26	04-Apr-26 A	05-Aug-26 A	494,887.02	494,887.02	494,887.02	-25
LANDSCAPE WORKS		251	29.28%	28.48%	24-May-26	30-Dec-26	17-May-26 A	21-Mar-27	2,490,604.58	2,422,398.61	8,505,184.90	-65
PLAYGROUND AREA		251	47.07%	49.89%	24-May-26	27-Dec-26	19-May-26 A	21-Mar-27	644,908.73	683,464.16	1,369,978.66	-68
FOOTBALL PLAYGROUND		209	35%	35%	24-May-26	13-Dec-26	19-May-26 A	26-Jan-27	110,897.50	110,897.50	316,849.99	-38
PADEL PLAYGROUND		189	45%	70%	20-Jun-26	19-Dec-26	19-May-26 A	26-Jan-27	105,292.80	163,788.80	233,984.00	-33
BASKETBALL PLAYGROUND		172	68.07%	69.52%	14-Jul-26	23-Dec-26	19-May-26 A	31-Jan-27	216,532.16	221,133.58	318,089.68	-33
PADEL FENCE		81	21.91%	4.22%	01-Sep-26	16-Nov-26	08-Aug-26 A	05-Dec-26	30,401.93	5,859.94	138,749.98	-16
CURBSTOEN/INTERLOCK		139	50.17%	50.17%	06-Oct-26	27-Dec-26	15-Aug-26 A	21-Mar-27	181,784.34	181,784.34	362,305.01	-68
AIR DOME		134	23.18%	23.18%	26-Sep-26	21-Dec-26	17-May-26 A	01-Mar-27	1,299,527.51	1,299,527.51	5,605,894.61	-59
CIVIL WORKS		101	48.29%	48.29%	26-Sep-26	07-Dec-26	17-May-26 A	20-Jan-27	1,299,527.51	1,299,527.51	2,690,829.42	-38
MECHANICAL WORKS		10	0%	0%	09-Dec-26	20-Dec-26	21-Jan-27	01-Feb-27	0.00	0.00	1,233,296.81	-37
ELECTRICAL WORKS		7	0%	0%	13-Dec-26	20-Dec-26	25-Jan-27	01-Feb-27	0.00	0.00	1,513,591.54	-37
FINISHES WORKS		6	0%	0%	15-Dec-26	21-Dec-26	23-Feb-27	01-Mar-27	0.00	0.00	168,176.84	-59
IRRIGATION NETWORK		169	83.53%	83.53%	28-Jun-26	30-Nov-26	18-Aug-26 A	11-Jan-27	127,308.67	127,308.67	152,414.87	-36
NATURAL GROUND		12	0%	0%	17-Nov-26	30-Nov-26	29-Dec-26	11-Jan-27	0.00	0.00	191,740.00	-36
PLANTING		15	59.18%	0%	17-Sep-26	31-Oct-26	17-Dec-26	03-Jan-27	205,518.96	0.00	347,251.46	-55
WALKING/BIKE PATHS		24	55.1%	50%	05-Oct-26	01-Nov-26	11-Jun-26 A	29-Dec-26	202,560.77	183,816.95	367,633.90	-49
GENERAL/FURNITURE		105	2.29%	27.28%	19-Oct-26	30-Dec-26	03-Oct-26 A	17-Feb-27	10,779.94	128,281.32	470,271.40	-42
PARKING		24	0%	100%	01-Nov-26	28-Nov-26	16-May-26 A	12-Oct-26 A	0.00	58,493.33	58,493.33	40
TOILET/SERVICE BUILDING		215	64.79%	51.37%	02-Jul-26	31-Dec-26	21-May-26 A	15-Mar-27	756,824.05	599,994.81	1,168,074.78	-59
STRUCTURE WORKS		58	100%	100%	02-Jul-26	07-Sep-26	21-May-26 A	02-Aug-26 A	162,899.73	162,899.73	162,899.73	31
MASONARY WORK		5	100%	100%	08-Sep-26	13-Sep-26	13-Jul-26 A	14-Jul-26 A	12,284.10	12,284.10	12,284.10	52
THERMAL & MOISTER PROTECTION		50	100%	76.27%	29-Aug-26	21-Sep-26	26-Sep-26 A	28-Oct-26	34,698.32	26,463.20	34,698.32	-31
MECHANICAL WORK		169	62.8%	48.91%	16-Jul-26	19-Dec-26	18-Jul-26 A	30-Jan-27	166,205.09	129,442.11	264,673.10	-36
ELECTRICAL WORKS		119	53.29%	53.29%	13-Sep-26	19-Dec-26	19-Jul-26 A	30-Jan-27	206,217.32	206,217.32	386,998.59	-36
DOORS/WINDOWS		122	88.57%	0%	17-Sep-26	31-Dec-26	20-Oct-26	15-Mar-27	60,445.68	0.00	68,245.12	-59
METAL WORKS		71	57.14%	28.57%	14-Sep-26	23-Nov-26	16-Sep-26 A	19-Dec-26	7,799.44	3,899.72	13,649.02	-22
FINISHING WORKS		105	60.45%	35.39%	22-Sep-26	12-Dec-26	10-Aug-26 A	23-Jan-27	100,424.79	58,788.63	166,130.97	-36
SPECIALTIES WORK		76	10%	0%	18-Oct-26	17-Dec-26	02-Nov-26	28-Jan-27	5,849.58	0.00	58,495.83	-36
TESTING & COMMISSIONING		17	0%	0%	20-Dec-26	02-Jan-27	27-Feb-27	21-Mar-27	0.00	0.00	0.00	-63
HASA OASIS		343	38.89%	43.28%	03-Mar-26	02-Jan-27	04-Mar-26 A	19-Apr-27	3,872,256.56	4,308,669.28	9,955,979.43	-88
MOBILIZATION		32	0%	0%	03-Mar-26	12-Apr-26	04-Mar-26 A	04-Apr-26 A	0.00	0.00	0.00	7
ENGINEERING		242	0%	0%	08-Mar-26	17-Dec-26	08-Mar-26 A	22-Dec-26	0.00	0.00	0.00	-4
PROCUREMENT		248	0%	0%	20-May-26	01-Dec-26	04-Apr-26 A	14-Mar-27	0.00	0.00	0.00	-84
CONSTRUCTION PHASE		322	38.89%	43.28%	29-Mar-26	31-Dec-26	04-Apr-26 A	17-Apr-27	3,872,256.56	4,308,669.28	9,955,979.43	-87
SITE WORKS		322	34.72%	39.78%	29-Mar-26	31-Dec-26	04-Apr-26 A	17-Apr-27	3,051,659.81	3,496,923.24	8,789,975.14	-87
EARTH WORKS		43	100%	100%	29-Mar-26	17-May-26	04-Apr-26 A	08-Aug-26 A	294,826.31	294,826.31	294,826.31	-67
LANDSCAPE WORKS		281	32.68%	37.26%	16-May-26	31-Dec-26	16-May-26 A	17-Apr-27	2,756,833.50	3,143,603.60	8,436,655.50	-87
PLAYGROUND AREA		281	72.82%	75.51%	16-May-26	31-Dec-26	18-May-26 A	17-Apr-27	947,725.32	982,763.36	1,301,449.27	-87
FOOTBALL PLAYGROUND		236	80%	85%	16-May-26	09-Dec-26	18-May-26 A	18-Feb-27	253,479.99	269,322.49	316,849.99	-61
PADEL PLAYGROUND		234	45%	70%	11-Jun-26	31-Dec-26	18-May-26 A	16-Mar-27	105,292.80	163,788.80	233,984.00	-60
BASKETBALL PLAYGROUND		212	67.98%	70.92%	07-Jul-26	31-Dec-26	18-May-26 A	16-Mar-27	226,647.52	236,425.54	333,381.64	-60
PADEL FENCE		117	0%	9.24%	28-Nov-26	31-Dec-26	06-Aug-26 A	17-Apr-27	0.00	5,077.72	54,928.63	-87
CURBSTOEN/INTERLOCK		19	100%	85.05%	09-Sep-26	01-Oct-26	12-Aug-26 A	22-Oct-26	362,305.01	308,148.81	362,305.01	-18
AIR DOME		203	23.18%	23.18%	30-Jul-26	10-Dec-26	16-May-26 A	29-Mar-27	1,299,527.51	1,299,527.51	5,605,894.61	-89
CIVIL WORKS		191	48.29%	48.29%	30-Jul-26	07-Dec-26	16-May-26 A	15-Mar-27	1,299,527.51	1,299,527.51	2,690,829.42	-80
MECHANICAL WORKS		15	0%	0%	21-Nov-26	07-Dec-26	09-Mar-27	29-Mar-27	0.00	0.00	1,233,296.81	-92
ELECTRICAL WORKS		8	0%	0%	02-Dec-26	10-Dec-26	21-Mar-27	29-Mar-27	0.00	0.00	1,513,591.54	-89
FINISHES WORKS		25	0%	0%	15-Nov-26	10-Dec-26	25-Feb-27	29-Mar-27	0.00	0.00	168,176.84	-89
IRRIGATION NETWORK		159	35.18%	83.53%	03-Sep-26	07-Dec-26	18-Jul-26 A	09-Mar-27	53,620.00	127,308.67	152,414.87	-78
NATURAL GROUND		15	0%	53.56%	29-Nov-26	07-Dec-26	13-Oct-26 A	25-Oct-26	0.00	102,696.00	191,740.00	37
PLANTING		101	0%	42%	24-Oct-26	02-Nov-26	03-Oct-26 A	22-Oct-26	0.00	145,845.61	347,251.46	9
WALKING/BIKE PATHS		16	100%	75%	29-Sep-26	17-Oct-26	01-Jun-26 A	20-Oct-26	367,633.90	275,725.43	367,633.90	-2

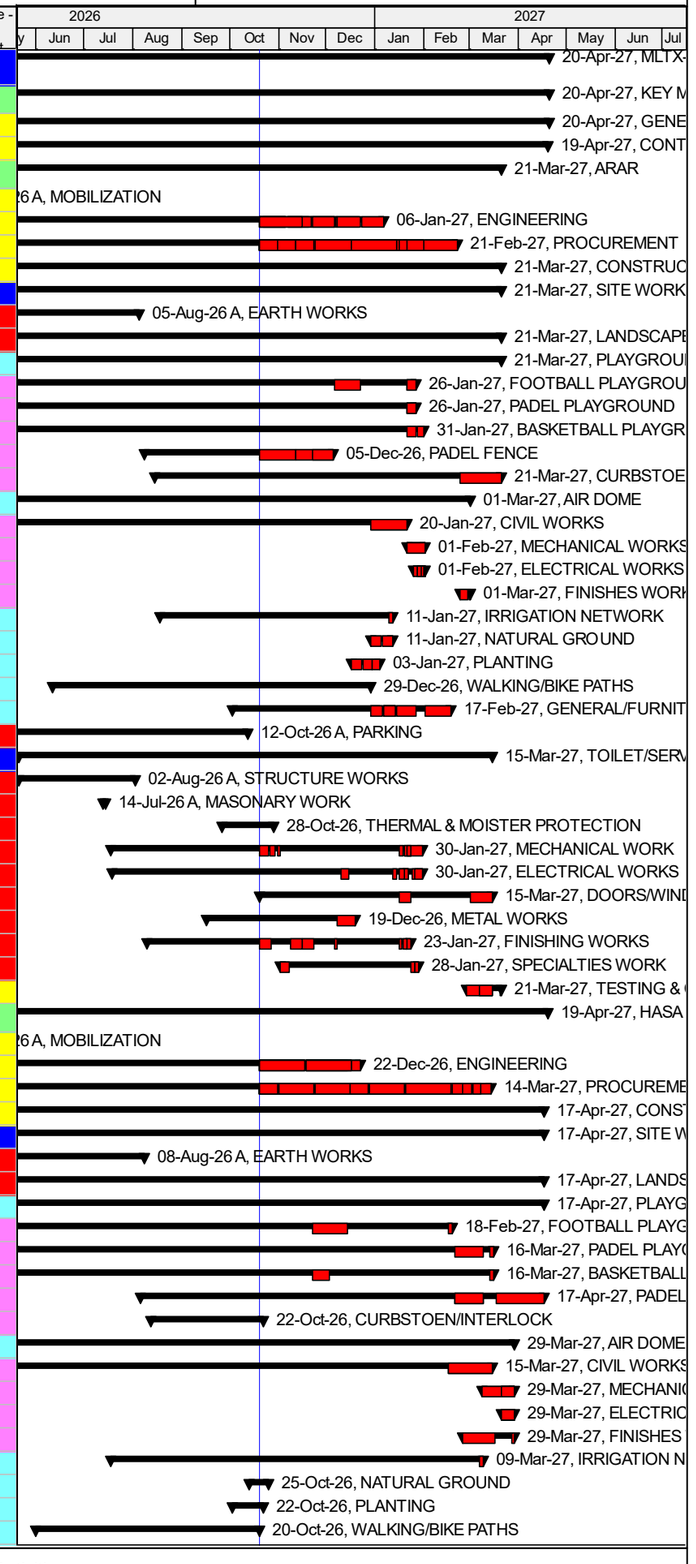

Remaining Work
Actual Work
Critical Remaining Work
Milestone
summary


TASK filter: All Activities

© Oracle Corporation

MLTX-02-005 - Playground Initiative for Eastern Region (Arar-Hasa osis -Dammam)

WBS Summary
D.D 19-10-2026

Activity ID	Activity Name	Original Duration	Schedule % Complete	Performance % Complete	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Variance - BL Project
	GENERAL/FURNITURE	139	18.78%	44.6%	06-Oct-26	24-Dec-26	03-Sep-26 A	21-Mar-27	88,326.76	209,737.02	470,271.40	-70
	PARKING	12	0%	100%	24-Nov-26	07-Dec-26	14-May-26 A	19-Sep-26 A	0.00	58,493.33	58,493.33	68
	TOILET/SERVICE BUILDING	271	70.38%	69.62%	09-May-26	23-Dec-26	24-May-26 A	29-Mar-27	820,596.75	811,746.04	1,166,004.29	-78
	STRUCTURE WORKS	45	100%	100%	09-May-26	02-Jul-26	24-May-26 A	10-Aug-26 A	162,899.73	162,899.73	162,899.73	-33
	MASONARY WORK	5	100%	100%	14-Jun-26	18-Jun-26	06-Jul-26 A	08-Jul-26 A	12,284.10	12,284.10	12,284.10	-16
	THERMAL & MOISTER PROTECTION	41	100%	95.21%	04-Jul-26	19-Aug-26	10-Sep-26 A	09-Nov-26	34,698.32	33,037.59	34,698.32	-69
	MECHANICAL WORK	171	98.48%	99.26%	24-Aug-26	21-Dec-26	12-Jul-26 A	16-Mar-27	260,651.49	262,723.23	264,673.10	-69
	ELECTRICAL WORKS	164	53.29%	53.29%	03-Sep-26	21-Dec-26	14-Jul-26 A	18-Mar-27	206,217.58	206,217.58	386,998.85	-71
	DOORS/WINDOWS	220	14.29%	14.29%	04-Jul-26	16-Dec-26	28-Sep-26 A	22-Mar-27	9,749.30	9,749.30	68,245.12	-78
	METAL WORKS	57	97.96%	71.43%	03-Sep-26	20-Oct-26	06-Sep-26 A	28-Nov-26	13,370.47	9,749.30	13,649.02	-33
	FINISHING WORKS	157	64.67%	63.02%	20-Aug-26	16-Dec-26	17-Aug-26 A	22-Mar-27	106,101.80	103,386.04	164,060.22	-78
	SPECIALTIES WORK	154	25%	20%	27-Sep-26	23-Dec-26	04-Oct-26 A	29-Mar-27	14,623.96	11,699.17	58,495.83	-78
	TESTING & COMMISSIONING	23	0%	0%	08-Dec-26	02-Jan-27	24-Mar-27	19-Apr-27	0.00	0.00	0.00	-88
	DAMMAM	313	39.18%	37.38%	03-Mar-26	02-Jan-27	04-Mar-26 A	15-Mar-27	3,845,653.74	3,669,187.59	9,815,232.20	-58
	MOBILIZATION	33	0%	0%	03-Mar-26	13-Apr-26	04-Mar-26 A	04-Apr-26 A	0.00	0.00	0.00	8
	ENGINEERING	256	0%	0%	09-Mar-26	12-Dec-26	08-Mar-26 A	09-Jan-27	0.00	0.00	0.00	-24
	PROCUREMENT	247	0%	0%	23-Apr-26	21-Dec-26	04-Apr-26 A	09-Feb-27	0.00	0.00	0.00	-43
	CONSTRUCTION PHASE	278	39.18%	37.38%	16-Apr-26	31-Dec-26	04-Apr-26 A	15-Mar-27	3,845,653.74	3,669,187.59	9,815,232.20	-59
	SITE WORKS	262	34.54%	33.06%	16-Apr-26	31-Dec-26	04-Apr-26 A	20-Feb-27	2,987,789.95	2,859,708.61	8,649,227.95	-43
	EARTH WORKS	44	100%	100%	16-Apr-26	09-Jun-26	04-Apr-26 A	13-Aug-26 A	263,237.78	263,237.78	263,237.78	-55
	LANDSCAPE WORKS	240	32.46%	30.48%	12-May-26	31-Dec-26	19-May-26 A	20-Feb-27	2,703,281.87	2,537,977.50	8,327,496.85	-43
	PLAYGROUND AREA	237	77.93%	53.08%	12-May-26	31-Dec-26	19-May-26 A	16-Feb-27	1,002,258.94	682,681.94	1,286,157.31	-40
	FOOTBALL PLAYGROUND	211	85%	35%	12-May-26	15-Dec-26	19-May-26 A	17-Jan-27	269,322.49	110,897.50	316,849.99	-28
	PADEL PLAYGROUND	222	70%	70%	24-May-26	24-Dec-26	19-May-26 A	10-Feb-27	163,788.80	163,788.80	233,984.00	-41
	BASKETBALL PLAYGROUND	173	65.03%	69.52%	26-Jul-26	31-Dec-26	19-May-26 A	13-Feb-27	206,842.64	221,133.58	318,089.68	-37
	PADEL FENCE	46	0%	9.24%	25-Nov-26	24-Dec-26	08-Aug-26 A	17-Jan-27	0.00	5,077.72	54,928.63	-20
	CURBSTOEN/INTERLOCK	148	100%	50.17%	27-Aug-26	21-Sep-26	10-Aug-26 A	16-Feb-27	362,305.01	181,784.34	362,305.01	-126
	AIR DOME	198	22.91%	23.18%	18-Jun-26	24-Dec-26	14-Jul-26 A	04-Feb-27	1,284,326.93	1,299,527.51	5,605,894.61	-36
	CIVIL WORKS	175	47.73%	48.29%	18-Jun-26	07-Dec-26	14-Jul-26 A	09-Jan-27	1,284,326.93	1,299,527.51	2,690,829.42	-28
	MECHANICAL WORKS	5	0%	0%	08-Dec-26	13-Dec-26	25-Jan-27	30-Jan-27	0.00	0.00	1,233,296.81	-41
	ELECTRICAL WORKS	10	0%	0%	08-Dec-26	24-Dec-26	25-Jan-27	04-Feb-27	0.00	0.00	1,513,591.54	-36
	FINISHES WORKS	4	0%	0%	12-Dec-26	15-Dec-26	28-Jan-27	01-Feb-27	0.00	0.00	168,176.84	-41
	IRRIGATION NETWORK	116	83.53%	83.53%	10-Sep-26	02-Dec-26	24-Aug-26 A	24-Jan-27	127,308.67	127,308.67	152,414.87	-45
	NATURAL GROUND	30	20.34%	0%	10-Oct-26	12-Nov-26	20-Oct-26	23-Nov-26	39,000.00	0.00	191,740.00	-9
	PLANTING	23	0%	0%	06-Dec-26	31-Dec-26	25-Jan-27	20-Feb-27	0.00	0.00	347,251.46	-43
	WALKING/BIKE PATHS	31	61.09%	100%	22-Sep-26	28-Oct-26	19-Jul-26 A	16-Sep-26 A	167,250.05	273,767.20	273,767.20	35
	GENERAL/FURNITURE	129	17.68%	32.89%	22-Sep-26	31-Dec-26	20-Sep-26 A	20-Feb-27	83,137.28	154,692.18	470,271.40	-43
	PARKING	15	36.36%	100%	14-Oct-26	31-Oct-26	18-Jul-26 A	19-Sep-26 A	21,270.30	58,493.33	58,493.33	35
	TOILET/SERVICE BUILDING	242	73.57%	69.42%	01-Jun-26	29-Dec-26	23-May-26 A	15-Mar-27	857,863.79	809,478.98	1,166,004.25	-61
	STRUCTURE WORKS	54	100%	100%	01-Jun-26	02-Aug-26	23-May-26 A	02-Aug-26 A	162,899.73	162,899.73	162,899.73	0
	MASONARY WORK	5	100%	100%	06-Jul-26	11-Jul-26	06-Jul-26 A	08-Jul-26 A	12,284.10	12,284.10	12,284.10	2
	THERMAL & MOISTER PROTECTION	21	100%	95.21%	03-Aug-26	26-Aug-26	25-Aug-26 A	28-Oct-26	34,698.32	33,037.59	34,698.32	-53
	MECHANICAL WORK	113	94.49%	99.26%	09-Sep-26	26-Dec-26	12-Jul-26 A	19-Jan-27	250,078.40	262,723.23	264,673.10	-21
	ELECTRICAL WORKS	136	53.29%	53.29%	12-Sep-26	29-Dec-26	14-Jul-26 A	17-Feb-27	206,217.55	206,217.55	386,998.82	-43
	DOORS/WINDOWS	121	91.43%	14.29%	19-Sep-26	27-Dec-26	17-Sep-26 A	07-Feb-27	62,395.54	9,749.30	68,245.12	-36
	METAL WORKS	69	87.76%	28.57%	10-Sep-26	26-Oct-26	05-Sep-26 A	14-Dec-26	11,977.71	3,899.72	13,649.02	-42
	FINISHING WORKS	114	71.51%	65.2%	27-Aug-26	21-Dec-26	17-Aug-26 A	21-Jan-27	117,312.45	106,968.59	164,060.21	-27
	SPECIALTIES WORK	63	0%	20%	27-Oct-26	23-Dec-26	12-Oct-26 A	15-Mar-27	0.00	11,699.17	58,495.83	-66
	TESTING & COMMISSIONING	23	0%	0%	24-Dec-26	02-Jan-27	13-Feb-27	15-Mar-27	0.00	0.00	0.00	-58
	PROJECT CLOSEOUT & DEMOBILIZATION	24	0%	0%	08-Dec-26	02-Jan-27	24-Mar-27	20-Apr-27	0.00	0.00	0.00	-89
	As-Built DWGs	20	0%	0%	08-Dec-26	31-Dec-26	24-Mar-27	15-Apr-27	0.00	0.00	0.00	-86
	Demobilization	8	0%	0%	28-Dec-26	02-Jan-27	12-Apr-27	20-Apr-27	0.00	0.00	0.00	-89

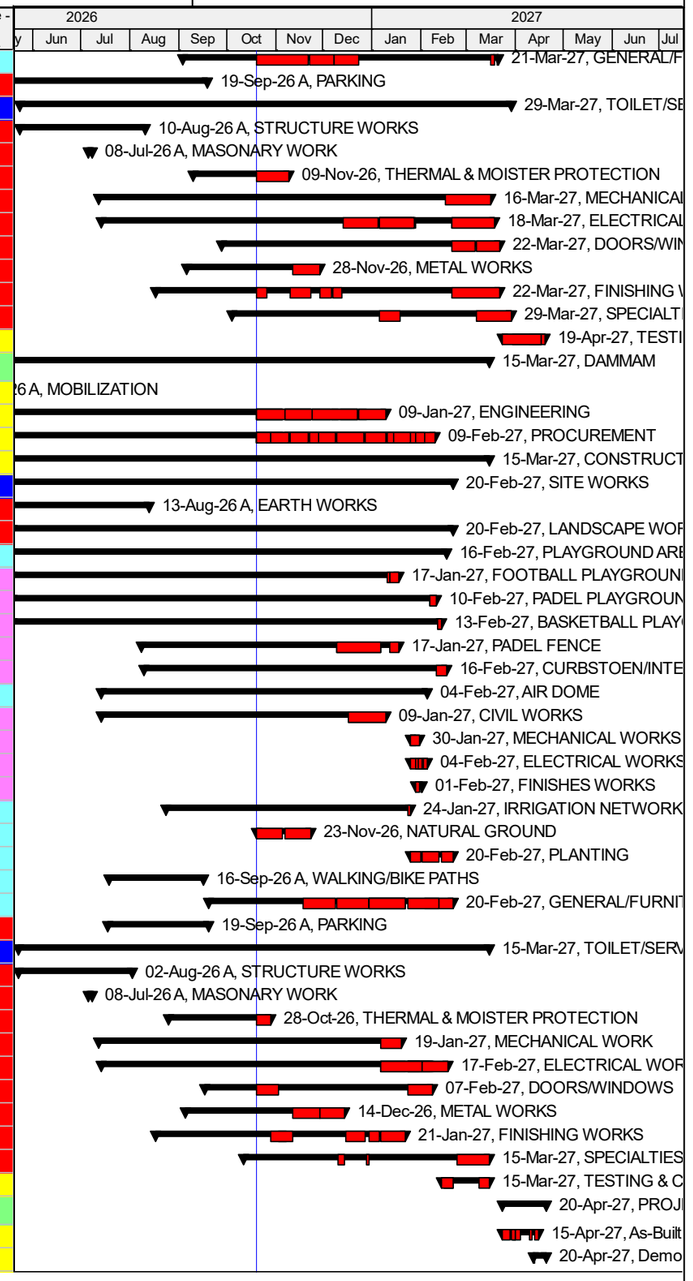

Remaining Work
Actual Work
Critical Remaining Work
Milestone
summary

TASK filter: All Activities

© Oracle Corporation
