
MLTX-02-005 - Playground Initiative for Eastern Region (Arar-Hasa osis -Dammam)

Remaining work
D.D 19-10-2026

Activity ID	Activity Name	Original Duration	Schedule % Complete	Performance % Complete	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Variance - BL Project
MLTX-02-005 Playground Initiative for Eastern Region (Arar - Hasa Oa		222	8.7%	6.12%	16-Apr-26	02-Jan-27	01-Jun-26 A	20-Apr-27	1,709,754.17	1,202,486.22	19,646,707.24	-89
KEY MILESTONES		83	0%	0%	17-Dec-26	02-Jan-27	09-Jan-27	20-Apr-27	0.00	0.00	0.00	-89
GENERAL MILESTONES		0	0%	0%	02-Jan-27	02-Jan-27	20-Apr-27	20-Apr-27	0.00	0.00	0.00	-89
MLTX-02-005-MS-1030	Project Completion	0	0%	0%		02-Jan-27		20-Apr-27	0.00	0.00	0.00	-89
CONTRACTUAL MILESTONE		82	0%	0%	17-Dec-26	02-Jan-27	09-Jan-27	19-Apr-27	0.00	0.00	0.00	-88
MLTX-02-005-MS-1070	Completion of Testing & Commissioning	0	0%	0%		02-Jan-27		19-Apr-27	0.00	0.00	0.00	-88
MLTX-02-005-MS-1100	Completion of Engineering	0	0%	0%		17-Dec-26		09-Jan-27	0.00	0.00	0.00	-19
MLTX-02-005-MS-1130	Completion of Toilet Building	0	0%	0%		31-Dec-26		17-Apr-27	0.00	0.00	0.00	-87
MLTX-02-005-MS-1140	Completion of Playground Area	0	0%	0%		31-Dec-26		17-Apr-27	0.00	0.00	0.00	-87
MLTX-02-005-MS-1150	Completion of Natural Landscape Works	0	0%	0%		31-Dec-26		17-Apr-27	0.00	0.00	0.00	-87
MLTX-02-005-MS-1160	Completion of Arar Works	0	0%	0%		31-Dec-26		21-Mar-27	0.00	0.00	0.00	-64
MLTX-02-005-MS-1170	Completion of Hasa Oasis Works	0	0%	0%		31-Dec-26		17-Apr-27	0.00	0.00	0.00	-87
MLTX-02-005-MS-1180	Completion of Dammam Works	0	0%	0%		31-Dec-26		15-Mar-27	0.00	0.00	0.00	-59
ARAR		158	8.77%	3.66%	27-Jun-26	02-Jan-27	11-Jun-26 A	21-Mar-27	605,622.54	252,810.25	6,903,676.50	-63
ENGINEERING		68	0%	0%	28-Jun-26	08-Dec-26	20-Oct-26	06-Jan-27	0.00	0.00	0.00	-25
SHOP DRAWINGS		68	0%	0%	28-Jun-26	08-Dec-26	20-Oct-26	06-Jan-27	0.00	0.00	0.00	-25
SHOP DRAWINGS SUBMISSION		42	0%	0%	19-Sep-26	07-Nov-26	20-Oct-26	07-Dec-26	0.00	0.00	0.00	-26
SHOP DRAWINGS SUBMITTALS FOR PLAYGROUND WORKS		42	0%	0%	19-Sep-26	07-Nov-26	20-Oct-26	07-Dec-26	0.00	0.00	0.00	-26
ELECTRICAL WORKS		42	0%	0%	19-Sep-26	07-Nov-26	20-Oct-26	07-Dec-26	0.00	0.00	0.00	-26
MLTX-02-005-EM	Shop DWG Submittal for Power Layout	27	96.3%	0%	19-Sep-26	20-Oct-26	20-Oct-26	19-Nov-26	0.00	0.00	0.00	-26
MLTX-02-005-EM	Shop DWG Submittal for Fire Alarm Layout	15	100%	0%	19-Sep-26	06-Oct-26	20-Oct-26	05-Nov-26	0.00	0.00	0.00	-26
MLTX-02-005-EM	Shop DWG Submittal for Fire Alarm Riser Diagram	15	0%	0%	21-Oct-26	07-Nov-26	21-Nov-26	07-Dec-26	0.00	0.00	0.00	-26
SHOP DRAWINGS APPROVALS		68	0%	0%	28-Jun-26	08-Dec-26	20-Oct-26	06-Jan-27	0.00	0.00	0.00	-25
SHOP DRAWINGS APPROVAL FOR PLAYGROUND WORKS		68	0%	0%	28-Jun-26	08-Dec-26	20-Oct-26	06-Jan-27	0.00	0.00	0.00	-25
ARCHITECTURE WORKS		26	0%	0%	15-Jul-26	13-Aug-26	07-Nov-26	06-Dec-26	0.00	0.00	0.00	-97
MLTX-02-005-EM	Shop DWG Approval for Dome Internal Layout	26	100%	0%	15-Jul-26	13-Aug-26	07-Nov-26	06-Dec-26	0.00	0.00	0.00	-97
AIR DOME SYSTEM		41	0%	0%	28-Jun-26	13-Aug-26	20-Oct-26	06-Dec-26	0.00	0.00	0.00	-97
MLTX-02-005-EM	Shop DWG Approval for Membrane Panel Layout	15	100%	0%	28-Jun-26	14-Jul-26	20-Oct-26	05-Nov-26	0.00	0.00	0.00	-97
MLTX-02-005-EM	Shop DWG Approval for Cable Tension Layout	13	100%	0%	30-Jun-26	14-Jul-26	22-Oct-26	05-Nov-26	0.00	0.00	0.00	-97
MLTX-02-005-EM	Shop DWG Approval for Airlock Door Details	13	100%	0%	15-Jul-26	29-Jul-26	07-Nov-26	21-Nov-26	0.00	0.00	0.00	-97
MLTX-02-005-EM	Shop DWG Approval for Emergency Exit Details	13	100%	0%	30-Jul-26	13-Aug-26	22-Nov-26	06-Dec-26	0.00	0.00	0.00	-97
SPORTS EQUIPMENT		13	0%	0%	15-Aug-26	29-Aug-26	07-Dec-26	21-Dec-26	0.00	0.00	0.00	-97
MLTX-02-005-EM	Shop DWG Approval for Football Turf Installation	13	100%	0%	15-Aug-26	29-Aug-26	07-Dec-26	21-Dec-26	0.00	0.00	0.00	-97
ELECTRICAL WORKS		68	0%	0%	26-Sep-26	08-Dec-26	20-Oct-26	06-Jan-27	0.00	0.00	0.00	-25
MLTX-02-005-EM	Shop DWG Approval for Lighting Layout	23	91.3%	0%	26-Sep-26	21-Oct-26	20-Oct-26	15-Nov-26	0.00	0.00	0.00	-21
MLTX-02-005-EM	Shop DWG Approval for Power Layout	13	0%	0%	09-Nov-26	23-Nov-26	08-Dec-26	22-Dec-26	0.00	0.00	0.00	-25
MLTX-02-005-EM	Shop DWG Approval for Power Installation Details	13	0%	0%	24-Nov-26	08-Dec-26	23-Dec-26	06-Jan-27	0.00	0.00	0.00	-25
PROCUREMENT		107	0%	0%	27-Jun-26	15-Dec-26	20-Oct-26	21-Feb-27	0.00	0.00	0.00	-58
SHORT LEAD ITEM		107	0%	0%	27-Jun-26	15-Dec-26	20-Oct-26	21-Feb-27	0.00	0.00	0.00	-58
TOILET/SERVICE WORKS		69	0%	0%	27-Jun-26	28-Nov-26	20-Oct-26	07-Jan-27	0.00	0.00	0.00	-35
LIGHTING FIXTURES		40	0%	0%	27-Jun-26	11-Aug-26	20-Oct-26	05-Dec-26	0.00	0.00	0.00	-98
MLTX-02-005-PR-E	Material Delivery for Lighting Fixtures	40	100%	0%	27-Jun-26	11-Aug-26	20-Oct-26	05-Dec-26	0.00	0.00	0.00	-98
SWITCHES/SOCKETS		42	0%	0%	22-Sep-26	28-Nov-26	20-Oct-26	07-Dec-26	0.00	0.00	0.00	-8
MLTX-02-005-PR-E	PO for Switches/Sockets	15	100%	0%	22-Sep-26	10-Oct-26	20-Oct-26	05-Nov-26	0.00	0.00	0.00	-23
MLTX-02-005-PR-E	Material Delivery for Switches/Sockets	27	0%	0%	28-Oct-26	28-Nov-26	07-Nov-26	07-Dec-26	0.00	0.00	0.00	-8
DISTRIBUTION PANNELS		44	0%	0%	27-Sep-26	20-Oct-26	20-Oct-26	09-Dec-26	0.00	0.00	0.00	-43
MLTX-02-005-PR-E	PO for Distribution Panels	5	100%	0%	27-Sep-26	01-Oct-26	20-Oct-26	25-Oct-26	0.00	0.00	0.00	-20
MLTX-02-005-PR-E	Material Delivery for Distribution Panels	15	93.33%	0%	04-Oct-26	20-Oct-26	23-Nov-26	09-Dec-26	0.00	0.00	0.00	-43
FURNITURES		69	0%	0%	30-Aug-26	19-Nov-26	20-Oct-26	07-Jan-27	0.00	0.00	0.00	-42
MLTX-02-005-PR-E	PO for Furnitures	29	100%	0%	30-Aug-26	03-Oct-26	20-Oct-26	22-Nov-26	0.00	0.00	0.00	-43
MLTX-02-005-PR-E	Material Delivery for Furnitures	40	32.5%	0%	05-Oct-26	19-Nov-26	23-Nov-26	07-Jan-27	0.00	0.00	0.00	-42
PLAYGROUND WORKS		107	0%	0%	15-Jul-26	15-Dec-26	20-Oct-26	21-Feb-27	0.00	0.00	0.00	-58
PVC MEMBRANE		21	0%	0%	29-Sep-26	22-Oct-26	07-Nov-26	30-Nov-26	0.00	0.00	0.00	-33
MLTX-02-005-PR-E	Material Delivery for PVC Membrane	21	85.71%	0%	29-Sep-26	22-Oct-26	07-Nov-26	30-Nov-26	0.00	0.00	0.00	-33
ARTIFICIAL TURF		12	0%	0%	26-Oct-26	08-Nov-26	18-Jan-27	31-Jan-27	0.00	0.00	0.00	-72
MLTX-02-005-PR-E	Material Delivery for Artificial TURF	12	0%	0%	26-Oct-26	08-Nov-26	18-Jan-27	31-Jan-27	0.00	0.00	0.00	-72
RUBBER GRANULES		32	0%	0%	10-Oct-26	15-Nov-26	07-Nov-26	13-Dec-26	0.00	0.00	0.00	-24
MLTX-02-005-PR-E	Material Delivery for Rubber Granules	32	28.13%	0%	10-Oct-26	15-Nov-26	07-Nov-26	13-Dec-26	0.00	0.00	0.00	-24
PADEL GLASS		18	0%	0%	16-Nov-26	06-Dec-26	01-Feb-27	21-Feb-27	0.00	0.00	0.00	-66
MLTX-02-005-PR-E	Material Delivery for Padel Glass	18	0%	0%	16-Nov-26	06-Dec-26	01-Feb-27	21-Feb-27	0.00	0.00	0.00	-66
PADEL WIRE MESH/STEEL SETS		15	0%	0%	31-Aug-26	16-Sep-26	20-Oct-26	05-Nov-26	0.00	0.00	0.00	-42
MLTX-02-005-PR-E	Material Delivery for Wire Mesh/Steel Sets	15	100%	0%	31-Aug-26	16-Sep-26	20-Oct-26	05-Nov-26	0.00	0.00	0.00	-42
BITUMINOUS BASE & WEARING COURSE		27	0%	0%	29-Sep-26	29-Oct-26	07-Nov-26	07-Dec-26	0.00	0.00	0.00	-33

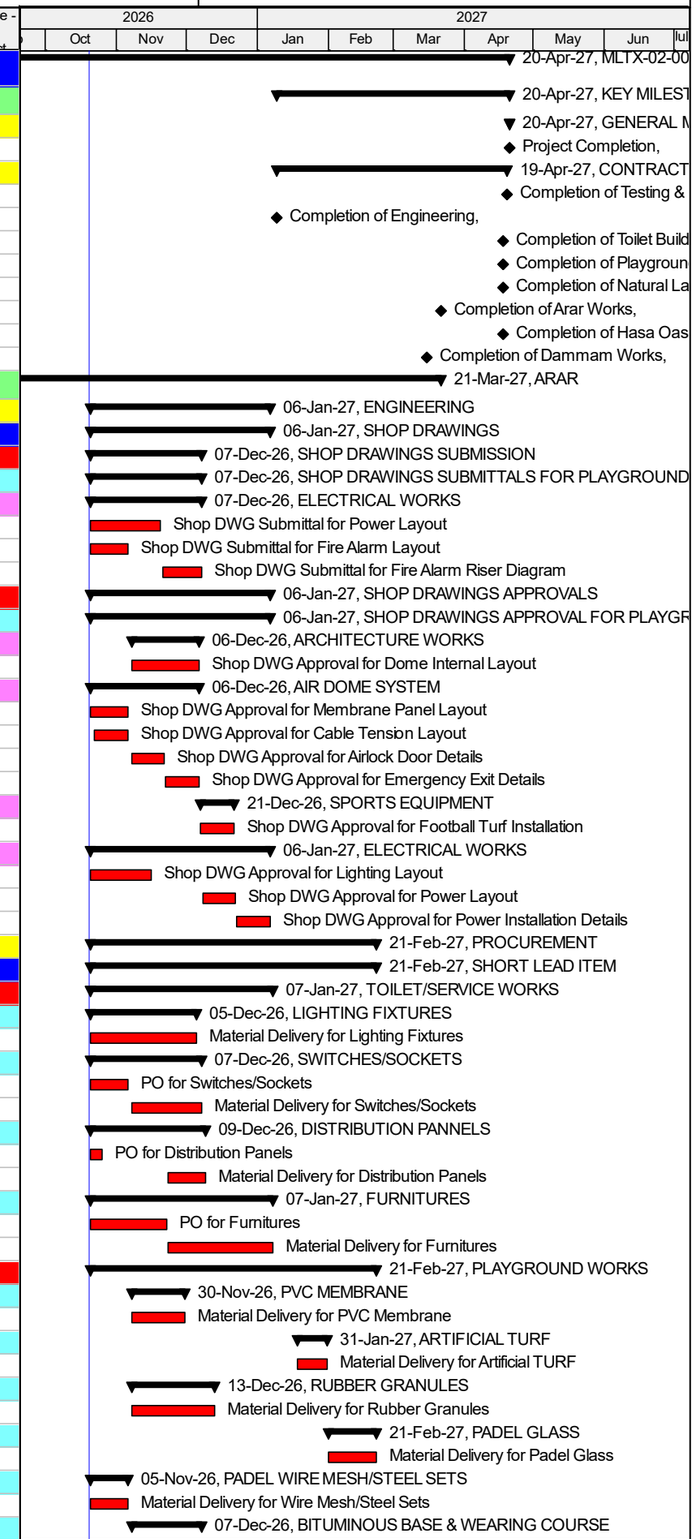

Remaining Work ◆ Milestone
Actual Work Critical Remaining Work summary


TASK filter: Remaining works.

© Oracle Corporation

MLTX-02-005 - Playground Initiative for Eastern Region (Arar-Hasa osis -Dammam)

Remaining work
D.D 19-10-2026

Activity ID	Activity Name	Original Duration	Schedule % Complete	Performance % Complete	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Variance - BL Project
MLTX-02-005-PR-9	Material Delivery for the Site	27	66.67%	0%	29-Sep-26	29-Oct-26	07-Nov-26	07-Dec-26	0.00	0.00	0.00	-33
INTERLOCKING PAVING		17	0%	0%	11-Nov-26	30-Nov-26	17-Dec-26	05-Jan-27	0.00	0.00	0.00	-31
MLTX-02-005-PR-9	Material Delivery for Interlocking Block Pavers	17	0%	0%	11-Nov-26	30-Nov-26	17-Dec-26	05-Jan-27	0.00	0.00	0.00	-31
MARKING PAINT		77	0%	0%	10-Sep-26	19-Oct-26	20-Oct-26	17-Jan-27	0.00	0.00	0.00	-77
MLTX-02-005-PR-9	PO for Marking Paint	15	100%	0%	10-Sep-26	28-Sep-26	20-Oct-26	05-Nov-26	0.00	0.00	0.00	-33
MLTX-02-005-PR-9	Material Delivery for Marking Paint	17	100%	0%	30-Sep-26	19-Oct-26	29-Dec-26	17-Jan-27	0.00	0.00	0.00	-77
AIR DIFUSSERS/GRILLS		20	0%	0%	29-Sep-26	21-Oct-26	07-Nov-26	29-Nov-26	0.00	0.00	0.00	-33
MLTX-02-005-PR-9	PO for Air Difussers/Grills	5	100%	0%	29-Sep-26	04-Oct-26	07-Nov-26	11-Nov-26	0.00	0.00	0.00	-33
MLTX-02-005-PR-9	Material Delivery for Air Difussers/Grills	15	86.67%	0%	05-Oct-26	21-Oct-26	12-Nov-26	29-Nov-26	0.00	0.00	0.00	-33
GALVANIZED DUCTS		20	0%	0%	29-Sep-26	21-Oct-26	07-Nov-26	29-Nov-26	0.00	0.00	0.00	-33
MLTX-02-005-PR-9	PO for Galvanized Duct	5	100%	0%	29-Sep-26	04-Oct-26	07-Nov-26	11-Nov-26	0.00	0.00	0.00	-33
MLTX-02-005-PR-9	Material Delivery for Galvanized Duct	15	86.67%	0%	05-Oct-26	21-Oct-26	12-Nov-26	29-Nov-26	0.00	0.00	0.00	-33
EXHAUST FANS		20	0%	0%	16-Sep-26	10-Oct-26	20-Oct-26	11-Nov-26	0.00	0.00	0.00	-28
MLTX-02-005-PR-9	PO for Exhaust Fans	5	100%	0%	16-Sep-26	21-Sep-26	20-Oct-26	25-Oct-26	0.00	0.00	0.00	-28
MLTX-02-005-PR-9	Material Delivery for Exhaust Fans	15	100%	0%	22-Sep-26	10-Oct-26	26-Oct-26	11-Nov-26	0.00	0.00	0.00	-28
DISTRIBUTION BOARDS		20	0%	0%	29-Sep-26	21-Oct-26	07-Nov-26	29-Nov-26	0.00	0.00	0.00	-33
MLTX-02-005-PR-9	PO for Distribution Boards	5	100%	0%	29-Sep-26	04-Oct-26	07-Nov-26	11-Nov-26	0.00	0.00	0.00	-33
MLTX-02-005-PR-9	Material Delivery for Distribution Boards	15	86.67%	0%	05-Oct-26	21-Oct-26	12-Nov-26	29-Nov-26	0.00	0.00	0.00	-33
POWER CABLES		60	0%	0%	05-Oct-26	15-Dec-26	12-Nov-26	20-Jan-27	0.00	0.00	0.00	-31
MLTX-02-005-PR-9	PO for Power Cables	5	100%	0%	05-Oct-26	10-Oct-26	12-Nov-26	17-Nov-26	0.00	0.00	0.00	-33
MLTX-02-005-PR-9	Material Delivery for Power Cables	30	0%	0%	11-Nov-26	15-Dec-26	17-Dec-26	20-Jan-27	0.00	0.00	0.00	-31
LIGHT FIXTURES		10	0%	0%	11-Oct-26	21-Oct-26	18-Nov-26	29-Nov-26	0.00	0.00	0.00	-33
MLTX-02-005-PR-9	Material Delivery for Light Fixtures	10	80%	0%	11-Oct-26	21-Oct-26	18-Nov-26	29-Nov-26	0.00	0.00	0.00	-33
CCTV MATERIALS		50	0%	0%	26-Sep-26	10-Nov-26	20-Oct-26	16-Dec-26	0.00	0.00	0.00	-31
MLTX-02-005-PR-9	PO for CCTV	25	84%	0%	26-Sep-26	24-Oct-26	20-Oct-26	17-Nov-26	0.00	0.00	0.00	-21
MLTX-02-005-PR-9	Material Delivery for CCTV	15	0%	0%	25-Oct-26	10-Nov-26	30-Nov-26	16-Dec-26	0.00	0.00	0.00	-31
POWER OUTLETS/SWITCHES		30	0%	0%	15-Jul-26	18-Aug-26	20-Oct-26	23-Nov-26	0.00	0.00	0.00	-82
MLTX-02-005-PR-9	Material Delivery for Power Outlets/Switches	30	100%	0%	15-Jul-26	18-Aug-26	20-Oct-26	23-Nov-26	0.00	0.00	0.00	-82
LANDSCAPE WORKS		107	0%	0%	15-Jul-26	23-Nov-26	20-Oct-26	21-Feb-27	0.00	0.00	0.00	-77
PAVEMENT MARKING		107	0%	0%	15-Jul-26	23-Nov-26	20-Oct-26	21-Feb-27	0.00	0.00	0.00	-77
MLTX-02-005-PR-9	PO for Pavement Markings	5	100%	0%	15-Jul-26	20-Jul-26	20-Oct-26	25-Oct-26	0.00	0.00	0.00	-82
MLTX-02-005-PR-9	Material Delivery for Pavement Markings	30	0%	0%	20-Oct-26	23-Nov-26	18-Jan-27	21-Feb-27	0.00	0.00	0.00	-77
TRAFFIC SIGNS		45	0%	0%	27-Jul-26	16-Sep-26	26-Oct-26	16-Dec-26	0.00	0.00	0.00	-77
MLTX-02-005-PR-9	PO for Traffic Signs	15	100%	0%	27-Jul-26	12-Aug-26	26-Oct-26	11-Nov-26	0.00	0.00	0.00	-77
MLTX-02-005-PR-9	Material Delivery for Traffic Signs	30	100%	0%	13-Aug-26	16-Sep-26	12-Nov-26	16-Dec-26	0.00	0.00	0.00	-77
AGRICULTURE SOIL		42	0%	0%	01-Aug-26	12-Sep-26	20-Oct-26	07-Dec-26	0.00	0.00	0.00	-73
MLTX-02-005-PR-9	PO for Agriculture Soil	15	100%	0%	01-Aug-26	17-Aug-26	20-Oct-26	05-Nov-26	0.00	0.00	0.00	-68
MLTX-02-005-PR-9	Material Delivery for Agriculture Soil	22	100%	0%	18-Aug-26	12-Sep-26	12-Nov-26	07-Dec-26	0.00	0.00	0.00	-73
TRACK SURFACE		10	0%	0%	17-Sep-26	29-Sep-26	17-Dec-26	28-Dec-26	0.00	0.00	0.00	-77
MLTX-02-005-PR-9	Material Delivery for Track Surface	10	100%	0%	17-Sep-26	29-Sep-26	17-Dec-26	28-Dec-26	0.00	0.00	0.00	-77
GRASS/TREES		25	0%	0%	20-Oct-26	17-Nov-26	07-Nov-26	05-Dec-26	0.00	0.00	0.00	-15
MLTX-02-005-PR-9	Material Delivery for Grass/Trees	25	0%	0%	20-Oct-26	17-Nov-26	07-Nov-26	05-Dec-26	0.00	0.00	0.00	-15
LONG LEAD ITEM		89	0%	0%	18-Aug-26	10-Dec-26	20-Oct-26	31-Jan-27	0.00	0.00	0.00	-44
PLAYGROUND WORKS		89	0%	0%	18-Aug-26	10-Dec-26	20-Oct-26	31-Jan-27	0.00	0.00	0.00	-44
STEEL TENSION CABLES		49	0%	0%	18-Aug-26	27-Oct-26	06-Dec-26	31-Jan-27	0.00	0.00	0.00	-82
MLTX-02-005-PR-8	PO for Steel Tension Cables	7	100%	0%	18-Aug-26	25-Aug-26	06-Dec-26	13-Dec-26	0.00	0.00	0.00	-93
MLTX-02-005-PR-8	Material Fabrication for Steel Tension Cables	15	100%	0%	08-Sep-26	26-Sep-26	14-Dec-26	30-Dec-26	0.00	0.00	0.00	-82
MLTX-02-005-PR-8	Material Delivery for Steel Tension Cables	15	100%	0%	27-Sep-26	13-Oct-26	31-Dec-26	17-Jan-27	0.00	0.00	0.00	-82
MLTX-02-005-PR-9	Staging time	12	41.67%	0%	14-Oct-26	27-Oct-26	18-Jan-27	31-Jan-27	0.00	0.00	0.00	-82
EMERGENCY DOORS		75	0%	0%	08-Sep-26	05-Dec-26	20-Oct-26	14-Jan-27	0.00	0.00	0.00	-35
MLTX-02-005-PR-8	PO for Emergency Doors	20	100%	0%	08-Sep-26	01-Oct-26	20-Oct-26	11-Nov-26	0.00	0.00	0.00	-35
MLTX-02-005-PR-8	Material Fabrication for Emergency Doors	20	75%	0%	03-Oct-26	25-Oct-26	12-Nov-26	05-Dec-26	0.00	0.00	0.00	-35
MLTX-02-005-PR-8	Material Delivery for Emergency Doors	20	0%	0%	26-Oct-26	17-Nov-26	06-Dec-26	28-Dec-26	0.00	0.00	0.00	-35
MLTX-02-005-PR-9	Staging time	15	0%	0%	18-Nov-26	05-Dec-26	29-Dec-26	14-Jan-27	0.00	0.00	0.00	-35
PRESSURE UNITS		70	0%	0%	08-Sep-26	29-Nov-26	20-Oct-26	09-Jan-27	0.00	0.00	0.00	-35
MLTX-02-005-PR-8	PO for Pressure Units	10	100%	0%	08-Sep-26	19-Sep-26	20-Oct-26	31-Oct-26	0.00	0.00	0.00	-35
MLTX-02-005-PR-8	Material Fabrication for Pressure Units	20	75%	0%	03-Oct-26	25-Oct-26	12-Nov-26	05-Dec-26	0.00	0.00	0.00	-35
MLTX-02-005-PR-8	Material Delivery for Pressure Units	25	0%	0%	26-Oct-26	23-Nov-26	06-Dec-26	03-Jan-27	0.00	0.00	0.00	-35
MLTX-02-005-PR-9	Staging time	5	0%	0%	24-Nov-26	29-Nov-26	04-Jan-27	09-Jan-27	0.00	0.00	0.00	-35
AIR LOCK DOORS		60	0%	0%	03-Oct-26	10-Dec-26	12-Nov-26	20-Jan-27	0.00	0.00	0.00	-35
MLTX-02-005-PR-8	PO for Lock Doors	10	100%	0%	03-Oct-26	13-Oct-26	12-Nov-26	23-Nov-26	0.00	0.00	0.00	-35
MLTX-02-005-PR-8	Material Fabrication for Lock Doors	20	25%	0%	14-Oct-26	05-Nov-26	24-Nov-26	16-Dec-26	0.00	0.00	0.00	-35
MLTX-02-005-PR-8	Material Delivery for Lock Doors	25	0%	0%	07-Nov-26	05-Dec-26	17-Dec-26	14-Jan-27	0.00	0.00	0.00	-35
MLTX-02-005-PR-9	Staging time	5	0%	0%	06-Dec-26	10-Dec-26	16-Jan-27	20-Jan-27	0.00	0.00	0.00	-35

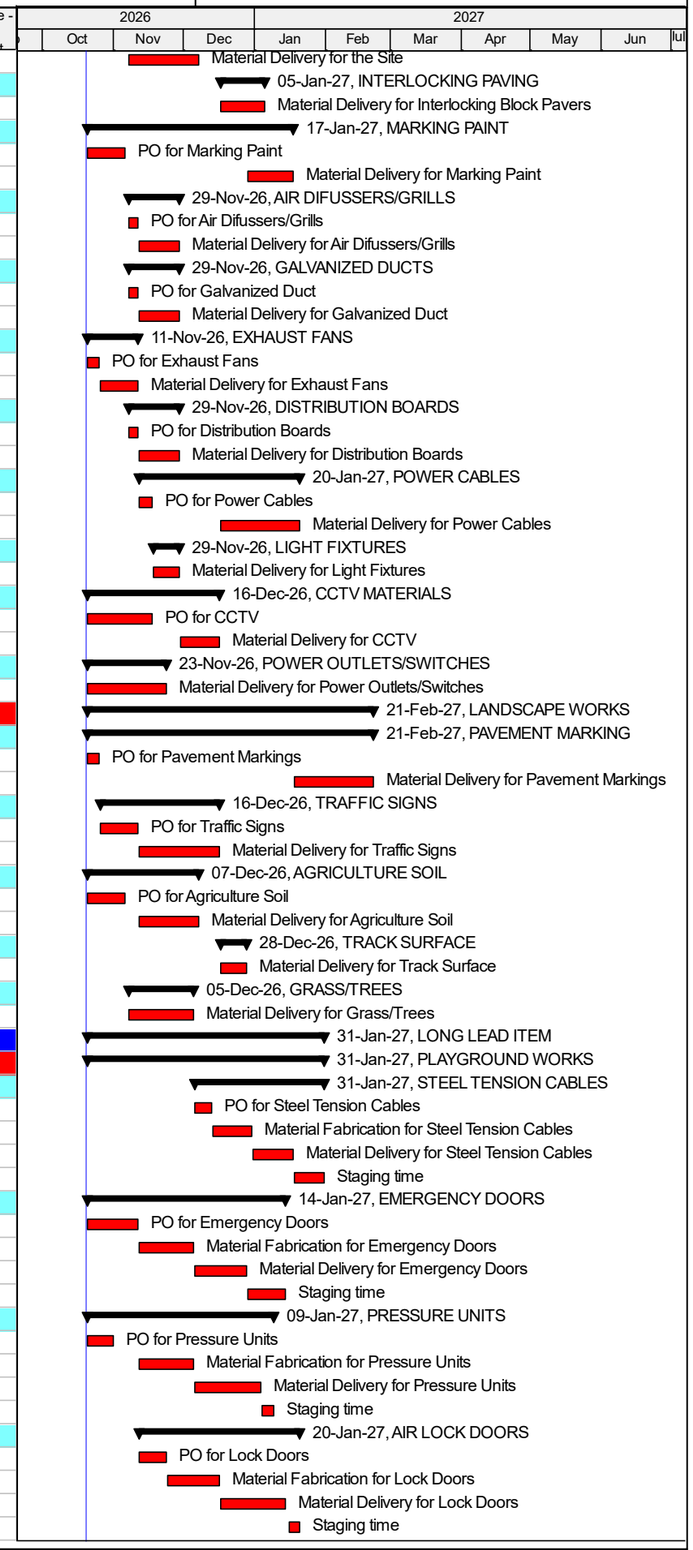

Remaining Work
Actual Work
Critical Remaining Work
Milestone
summary

TASK filter: Remaining works.

© Oracle Corporation

MLTX-02-005 - Playground Initiative for Eastern Region (Arar-Hasa osis -Dammam)


Remaining work
D.D 19-10-2026

PROFAST شركة برو فاست المحدودة

egis

MODON مدن

Activity ID	Activity Name	Original Duration	Schedule % Complete	Performance % Complete	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Variance - BL Project
CONSTRUCTION PHASE		158	8.77%	3.66%	31-Aug-26	31-Dec-26	11-Jun-26 A	21-Mar-27	605,622.54	252,810.25	6,903,676.50	-64
SITE WORKS		140	6.85%	3.74%	17-Sep-26	30-Dec-26	11-Jun-26 A	21-Mar-27	432,621.71	236,638.67	6,319,424.95	-65
LANDSCAPE WORKS		140	6.85%	3.74%	17-Sep-26	30-Dec-26	11-Jun-26 A	21-Mar-27	432,621.71	236,638.67	6,319,424.95	-65
PLAYGROUND AREA		127	3.57%	0%	01-Oct-26	27-Dec-26	20-Oct-26	21-Mar-27	24,541.99	0.00	686,514.50	-68
FOOTBALL PLAYGROUND		45	0%	0%	17-Nov-26	13-Dec-26	06-Dec-26	26-Jan-27	0.00	0.00	205,952.49	-38
MLTX-02-005-CI	Finishing Asphalt & Concrete Surface (Football Playground)	15	0%	0%	17-Nov-26	03-Dec-26	06-Dec-26	22-Dec-26	0.00	0.00	158,424.99	-16
MLTX-02-005-CI	Install Sport Equipments - Goal / Nets - (Football Playground)	5	0%	0%	08-Dec-26	13-Dec-26	21-Jan-27	26-Jan-27	0.00	0.00	31,685.00	-38
MLTX-02-005-CI	Surface Marking and Painting Finishing Work (Football	5	0%	0%	08-Dec-26	13-Dec-26	21-Jan-27	26-Jan-27	0.00	0.00	15,842.50	-38
PADEL PLAYGROUND		5	0%	0%	14-Dec-26	19-Dec-26	21-Jan-27	26-Jan-27	0.00	0.00	70,195.20	-33
MLTX-02-005-CI	Install Sport Equipments - Goal / Nets - (Padel Playground)	5	0%	0%	14-Dec-26	19-Dec-26	21-Jan-27	26-Jan-27	0.00	0.00	58,496.00	-33
MLTX-02-005-CI	Surface Marking and Painting Finishing Work (Padel	5	0%	0%	14-Dec-26	19-Dec-26	21-Jan-27	26-Jan-27	0.00	0.00	11,699.20	-33
BASKETBALL PLAYGROUND		9	0%	0%	14-Dec-26	23-Dec-26	21-Jan-27	31-Jan-27	0.00	0.00	96,956.10	-33
MLTX-02-005-CI	Install Sport Equipments - Goal / Nets - (Basketball	5	0%	0%	14-Dec-26	19-Dec-26	21-Jan-27	26-Jan-27	0.00	0.00	80,796.75	-33
MLTX-02-005-CI	Surface Marking and Painting Finishing Work (Basketball	4	0%	0%	20-Dec-26	23-Dec-26	27-Jan-27	31-Jan-27	0.00	0.00	16,159.35	-33
PADEL FENCE		40	18.47%	0%	01-Oct-26	16-Nov-26	20-Oct-26	05-Dec-26	24,541.99	0.00	132,890.04	-16
MLTX-02-005-CI	Tempered Glass Fenc Installation and Fixation	20	80%	0%	01-Oct-26	24-Oct-26	20-Oct-26	11-Nov-26	24,541.99	0.00	30,677.48	-16
MLTX-02-005-CI	Chain Link Fence Installation and Fixation	20	0%	0%	25-Oct-26	16-Nov-26	12-Nov-26	05-Dec-26	0.00	0.00	15,338.75	-16
MLTX-02-005-CI	Install of Fence Gates	12	0%	0%	03-Nov-26	16-Nov-26	22-Nov-26	05-Dec-26	0.00	0.00	86,873.81	-16
CURBSTOEN/INTERLOCK		20	0%	0%	05-Dec-26	27-Dec-26	23-Feb-27	21-Mar-27	0.00	0.00	180,520.67	-68
MLTX-02-005-CI	Interlock Installation (Grey Scale) for LandScape (Including	20	0%	0%	05-Dec-26	27-Dec-26	23-Feb-27	21-Mar-27	0.00	0.00	180,520.67	-68
AIR DOME		53	0%	0%	15-Nov-26	21-Dec-26	29-Dec-26	01-Mar-27	0.00	0.00	4,306,367.09	-59
CIVIL WORKS		20	0%	0%	15-Nov-26	07-Dec-26	29-Dec-26	20-Jan-27	0.00	0.00	1,391,301.90	-38
MLTX-02-005-CI	Install of Membrane Covering System (Air Dome)	20	0%	0%	15-Nov-26	07-Dec-26	29-Dec-26	20-Jan-27	0.00	0.00	942,830.33	-38
MLTX-02-005-CI	Thermal Insulation Works (Air Dome)	20	0%	0%	15-Nov-26	07-Dec-26	29-Dec-26	20-Jan-27	0.00	0.00	448,471.57	-38
MECHANICAL WORKS		10	0%	0%	09-Dec-26	20-Dec-26	21-Jan-27	01-Feb-27	0.00	0.00	1,233,296.81	-37
MLTX-02-005-CI	Air Ducts and Grills Installation (Air Dome)	10	0%	0%	09-Dec-26	20-Dec-26	21-Jan-27	01-Feb-27	0.00	0.00	728,766.30	-37
MLTX-02-005-CI	Air Units Installation (Air Dome)	10	0%	0%	09-Dec-26	20-Dec-26	21-Jan-27	01-Feb-27	0.00	0.00	336,353.67	-37
MLTX-02-005-CI	Exhaust Fans and Ducts Installation (Air Dome)	10	0%	0%	09-Dec-26	20-Dec-26	21-Jan-27	01-Feb-27	0.00	0.00	168,176.84	-37
ELECTRICAL WORKS		7	0%	0%	13-Dec-26	20-Dec-26	25-Jan-27	01-Feb-27	0.00	0.00	1,513,591.54	-37
MLTX-02-005-CI	Light Fixture Works (Air Dome)	7	0%	0%	13-Dec-26	20-Dec-26	25-Jan-27	01-Feb-27	0.00	0.00	224,235.78	-37
MLTX-02-005-CI	Distribution Board and Electrical Works (Air Dome)	5	0%	0%	15-Dec-26	20-Dec-26	27-Jan-27	01-Feb-27	0.00	0.00	168,176.84	-37
MLTX-02-005-CI	External Electrical Connection Works (Air Dome)	5	0%	0%	15-Dec-26	20-Dec-26	27-Jan-27	01-Feb-27	0.00	0.00	168,176.84	-37
MLTX-02-005-CI	Emergency Generator Installation (Air Dome)	3	0%	0%	17-Dec-26	20-Dec-26	30-Jan-27	01-Feb-27	0.00	0.00	504,530.51	-37
MLTX-02-005-CI	Control System Installation (Air Dome)	2	0%	0%	19-Dec-26	20-Dec-26	31-Jan-27	01-Feb-27	0.00	0.00	448,471.57	-37
FINISHES WORKS		6	0%	0%	15-Dec-26	21-Dec-26	23-Feb-27	01-Mar-27	0.00	0.00	168,176.84	-59
MLTX-02-005-CI	Doors Installation Including Emergency, Entrance doors (Air	5	0%	0%	15-Dec-26	20-Dec-26	23-Feb-27	28-Feb-27	0.00	0.00	112,117.89	-59
MLTX-02-005-CI	Logo and Signs Installation (Air Dome)	1	0%	0%	21-Dec-26	21-Dec-26	01-Mar-27	01-Mar-27	0.00	0.00	56,058.95	-59
IRRIGATION NETWORK		3	0%	0%	28-Nov-26	30-Nov-26	09-Jan-27	11-Jan-27	0.00	0.00	25,106.20	-36
MLTX-02-005-CN-1	Installing of Bubblers and Spreyers	3	0%	0%	28-Nov-26	30-Nov-26	09-Jan-27	11-Jan-27	0.00	0.00	25,106.20	-36
NATURAL GROUND		12	0%	0%	17-Nov-26	30-Nov-26	29-Dec-26	11-Jan-27	0.00	0.00	191,740.00	-36
MLTX-02-005-CN-1	Tartan Floor Installation Works for Landscape (Including	6	0%	0%	24-Nov-26	30-Nov-26	05-Jan-27	11-Jan-27	0.00	0.00	126,740.00	-36
MLTX-02-005-CN-1	Compacted Natural Ground Soil Installation Works for	6	0%	0%	17-Nov-26	23-Nov-26	29-Dec-26	04-Jan-27	0.00	0.00	65,000.00	-36
PLANTING		15	59.18%	0%	17-Sep-26	31-Oct-26	17-Dec-26	03-Jan-27	205,518.96	0.00	347,251.46	-55
MLTX-02-005-CN-1	Placement of Sweet/Agricultural Soil (Including Levelling and	6	100%	0%	17-Sep-26	24-Sep-26	17-Dec-26	23-Dec-26	104,175.44	0.00	104,175.44	-77
MLTX-02-005-CN-1	Placement of Lawn Ground Cover (Rolling and Compaction)	4	0%	0%	27-Oct-26	31-Oct-26	30-Dec-26	03-Jan-27	0.00	0.00	141,732.50	-55
MLTX-02-005-CN-1	Placement and Fixation of Trees	5	100%	0%	26-Sep-26	30-Sep-26	24-Dec-26	29-Dec-26	101,343.52	0.00	101,343.52	-77
WALKING/BIKE PATHS		24	55.1%	50%	05-Oct-26	01-Nov-26	11-Jun-26 A	29-Dec-26	202,560.77	183,816.95	367,633.90	-49
MLTX-02-005-CN-1	Bike Path Preparation and Installation Works	12	100%	50%	05-Oct-26	18-Oct-26	11-Jun-26 A	29-Dec-26	187,554.12	93,777.06	187,554.12	-61
MLTX-02-005-CN-1	Walking Path Preparation and Installation Works	12	8.33%	50%	19-Oct-26	01-Nov-26	11-Jun-26 A	29-Dec-26	15,006.65	90,039.89	180,079.78	-49
GENERAL/FURNITURE		44	0%	13.38%	27-Oct-26	30-Dec-26	18-Oct-26 A	17-Feb-27	0.00	52,821.72	394,811.80	-42
MLTX-02-005-CN-1	Stamped Concrete Works for LandScape (Including	5	0%	0%	02-Nov-26	07-Nov-26	29-Dec-26	03-Jan-27	0.00	0.00	93,594.00	-49
MLTX-02-005-CN-1	Traffic Signs Posts and Poles Installation	15	0%	0%	14-Dec-26	30-Dec-26	01-Feb-27	17-Feb-27	0.00	0.00	9,749.30	-42
MLTX-02-005-CN-1	Fixation and Installation of Steel Frame for Benches	7	0%	0%	27-Oct-26	03-Nov-26	29-Dec-26	05-Jan-27	0.00	0.00	17,274.79	-54
MLTX-02-005-CN-1	Fixation and Installation of Benches	7	0%	0%	23-Nov-26	30-Nov-26	06-Jan-27	13-Jan-27	0.00	0.00	40,307.84	-38
MLTX-02-005-CN-1	Fixation and Installation of Precast Concrete Seats	7	0%	0%	23-Nov-26	30-Nov-26	06-Jan-27	13-Jan-27	0.00	0.00	32,757.76	-38
MLTX-02-005-CN-1	Fixation and Installation of Precast Concrete Seats (Circular)	7	0%	0%	23-Nov-26	30-Nov-26	06-Jan-27	13-Jan-27	0.00	0.00	12,869.04	-38
MLTX-02-005-CN-1	Fixation and Installation of Precast Concrete Trash Bins	11	0%	0%	01-Dec-26	13-Dec-26	14-Jan-27	26-Jan-27	0.00	0.00	12,186.67	-38
MLTX-02-005-CN-1	Installing of Site Light Poles	13	0%	30%	08-Nov-26	22-Nov-26	18-Oct-26 A	03-Nov-26	0.00	52,821.72	176,072.40	16
TOILET/SERVICE BUILDING		153	29.61%	2.77%	31-Aug-26	31-Dec-26	03-Oct-26 A	15-Mar-27	173,000.82	16,171.58	584,251.55	-59
THERMAL & MOISTER PROTECTION		37	100%	61.73%	31-Aug-26	21-Sep-26	03-Oct-26 A	28-Oct-26	21,520.94	13,285.82	21,520.94	-31
MLTX-02-005-CN-11C	Finalize Water Proofing Works for Toilets	6	100%	0%	31-Aug-26	06-Sep-26	20-Oct-26	26-Oct-26	4,913.66	0.00	4,913.66	-42
MLTX-02-005-CN-11C	Finalize Water Proofing Works for Roofing and Wet Areas	8	100%	80%	13-Sep-26	21-Sep-26	03-Oct-26 A	28-Oct-26	16,607.28	13,285.82	16,607.28	-31
MECHANICAL WORK		88	27.19%	0%	29-Sep-26	19-Dec-26	20-Oct-26	30-Jan-27	36,762.98	0.00	135,230.99	-36
HVAC SYSTEM		3	0%	0%	05-Dec-26	07-Dec-26	16-Jan-27	18-Jan-27	0.00	0.00	14,623.96	-36

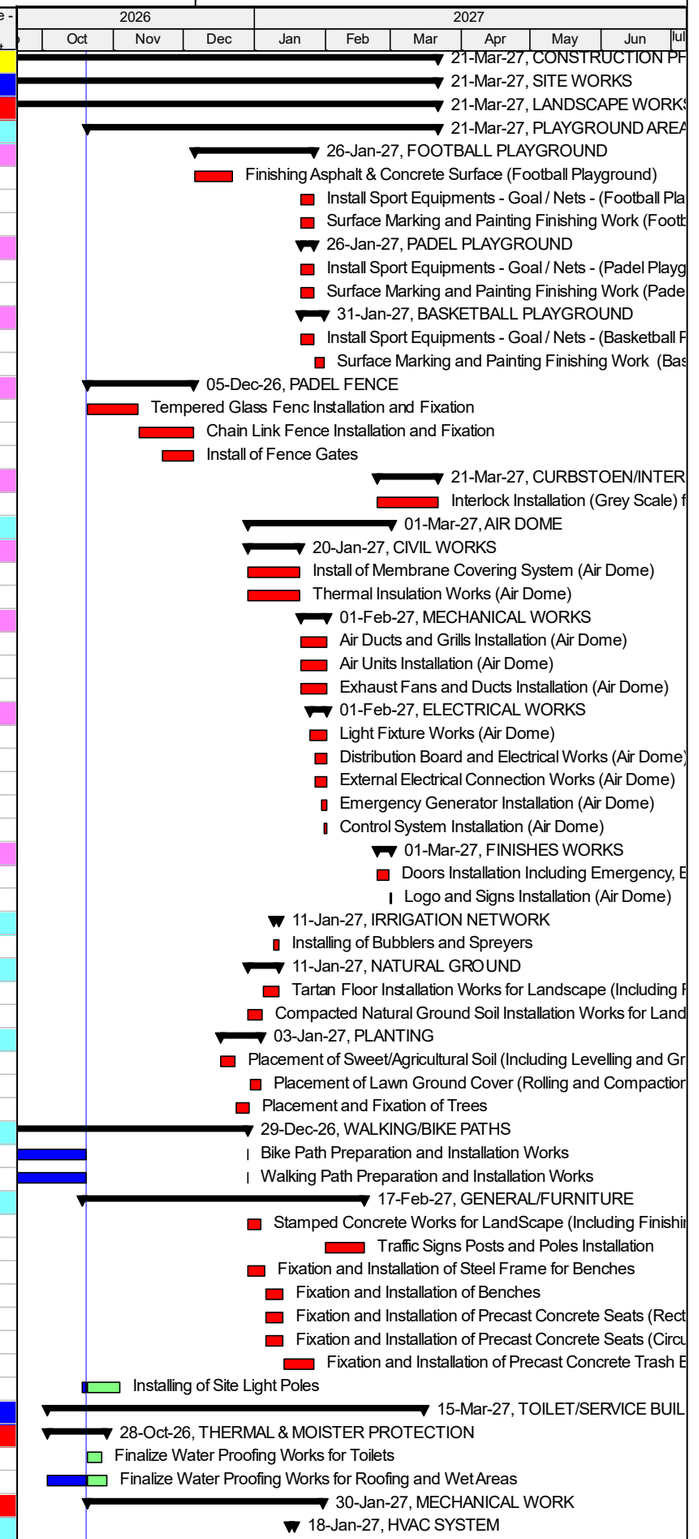

Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary


TASK filter: Remaining works.

© Oracle Corporation

MLTX-02-005 - Playground Initiative for Eastern Region (Arar-Hasa osis -Dammam)

Remaining work
D.D 19-10-2026

Activity ID	Activity Name	Original Duration	Schedule % Complete	Performance % Complete	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Variance - BL Project
MLTX-02-005-CN-1	Install and Finish HVAC and Ventilation Works Including Split	3	0%	0%	05-Dec-26	07-Dec-26	16-Jan-27	18-Jan-27	0.00	0.00	14,623.96	-36
WATER SUPPLY SYSTEM		10	0%	0%	08-Dec-26	19-Dec-26	19-Jan-27	30-Jan-27	0.00	0.00	50,501.39	-36
MLTX-02-005-CN-1	Installing of Booster Pump Units Including fittings and	7	0%	0%	12-Dec-26	19-Dec-26	23-Jan-27	30-Jan-27	0.00	0.00	48,746.52	-36
MLTX-02-005-CN-1	Installing of Water Heater	4	0%	0%	08-Dec-26	12-Dec-26	19-Jan-27	23-Jan-27	0.00	0.00	1,754.87	-36
SEWER/DRAINAGE SYSTEM		82	53.94%	0%	29-Sep-26	12-Dec-26	20-Oct-26	23-Jan-27	36,762.98	0.00	68,155.77	-36
MLTX-02-005-CN-1	Installing UPVC Pipes for External Connection for Sewage	4	100%	0%	05-Oct-26	08-Oct-26	26-Oct-26	29-Oct-26	14,217.67	0.00	14,217.67	-18
MLTX-02-005-CN-1	Installing of Plumping Fixtures and Accessories	2	100%	0%	15-Oct-26	17-Oct-26	31-Oct-26	01-Nov-26	10,358.68	0.00	10,358.68	-13
MLTX-02-005-CN-1	Installing Inspection Chamber for Sewage Network	5	100%	0%	29-Sep-26	04-Oct-26	20-Oct-26	25-Oct-26	12,186.63	0.00	12,186.63	-18
MLTX-02-005-CN-1	Installing of Toilet Fixtures and Accessories Such as Closets	4	0%	0%	08-Dec-26	12-Dec-26	19-Jan-27	23-Jan-27	0.00	0.00	31,392.79	-36
FIRE PROTECTION		2	0%	0%	14-Dec-26	15-Dec-26	21-Jan-27	23-Jan-27	0.00	0.00	1,949.87	-33
MLTX-02-005-CN-1	Installing of Fire Fighting Extinguisher and accessories	2	0%	0%	14-Dec-26	15-Dec-26	21-Jan-27	23-Jan-27	0.00	0.00	1,949.87	-33
ELECTRICAL WORKS		44	0%	0%	09-Nov-26	19-Dec-26	10-Dec-26	30-Jan-27	0.00	0.00	180,781.27	-36
FIXTURE WORKS		44	0%	0%	09-Nov-26	19-Dec-26	10-Dec-26	30-Jan-27	0.00	0.00	180,781.27	-36
MLTX-02-005-CN-1	Installing and Finish Works of Panel Boards	5	0%	0%	09-Nov-26	14-Nov-26	10-Dec-26	15-Dec-26	0.00	0.00	102,367.69	-27
MLTX-02-005-CN-1	Installing Data and Telecommunication System with all	4	0%	0%	13-Dec-26	16-Dec-26	24-Jan-27	27-Jan-27	0.00	0.00	6,239.59	-36
MLTX-02-005-CN-1	Installing and Finalize Works of Sockets and Power Points	4	0%	0%	07-Dec-26	10-Dec-26	18-Jan-27	21-Jan-27	0.00	0.00	7,085.10	-36
MLTX-02-005-CN-1	Installing and Finalize Works of Earthing Works	3	0%	0%	01-Dec-26	03-Dec-26	12-Jan-27	14-Jan-27	0.00	0.00	6,824.51	-36
MLTX-02-005-CN-1	Installing of Fire automation and Fire Alarm System	4	0%	0%	15-Dec-26	19-Dec-26	26-Jan-27	30-Jan-27	0.00	0.00	34,317.53	-36
MLTX-02-005-CN-1	Installing and Finalize Works of Lighting Works including Light	4	0%	0%	07-Dec-26	10-Dec-26	18-Jan-27	21-Jan-27	0.00	0.00	14,259.43	-36
MLTX-02-005-CN-1	Installing and Finalize Works of Lightning Protection System	6	0%	0%	05-Dec-26	10-Dec-26	16-Jan-27	21-Jan-27	0.00	0.00	2,437.33	-36
MLTX-02-005-CN-1	Installing and Finalize Works of Security and Access Control	4	0%	0%	05-Dec-26	08-Dec-26	16-Jan-27	19-Jan-27	0.00	0.00	7,250.09	-36
DOORS/WINDOWS		122	88.57%	0%	17-Sep-26	31-Dec-26	20-Oct-26	15-Mar-27	60,445.68	0.00	68,245.12	-59
MLTX-02-005-CN-111	Preliminary Works For Windows/Curtain Wall	2	100%	0%	17-Sep-26	19-Sep-26	20-Oct-26	21-Oct-26	52,646.24	0.00	52,646.24	-27
MLTX-02-005-CN-111	Preliminary Works For Doors	3	100%	0%	20-Sep-26	22-Sep-26	22-Oct-26	25-Oct-26	7,799.44	0.00	7,799.44	-27
MLTX-02-005-CN-111	Finalize Metal Doors for Toilets Building	9	0%	0%	22-Dec-26	31-Dec-26	02-Mar-27	15-Mar-27	0.00	0.00	1,949.86	-59
MLTX-02-005-CN-111	Finalize Glazzed Curtain Wall Works	7	0%	0%	05-Dec-26	12-Dec-26	16-Jan-27	23-Jan-27	0.00	0.00	5,849.58	-36
METAL WORKS		52	40%	0%	14-Sep-26	23-Nov-26	20-Oct-26	19-Dec-26	3,899.72	0.00	9,749.30	-22
MLTX-02-005-CN-111	Installation of Galvanized Steel Ladder	10	0%	0%	12-Nov-26	23-Nov-26	08-Dec-26	19-Dec-26	0.00	0.00	5,849.58	-22
MLTX-02-005-CN-111	Installation of DI Cover for Tank	4	100%	0%	14-Sep-26	17-Sep-26	20-Oct-26	24-Oct-26	3,899.72	0.00	3,899.72	-30
FINISHING WORKS		82	40.39%	2.62%	06-Oct-26	12-Dec-26	19-Oct-26 A	23-Jan-27	44,521.92	2,885.76	110,228.10	-36
FLOOR FINISHES		82	71.43%	0%	06-Oct-26	12-Dec-26	20-Oct-26	23-Jan-27	2,924.82	0.00	4,094.76	-36
MLTX-02-005-CN-1	Granite Tiles Floor Finish Works	4	100%	0%	06-Oct-26	10-Oct-26	20-Oct-26	24-Oct-26	2,924.82	0.00	2,924.82	-12
MLTX-02-005-CN-1	Epoxy Coat on Concrete Floor	3	0%	0%	09-Dec-26	12-Dec-26	20-Jan-27	23-Jan-27	0.00	0.00	1,169.94	-36
WALL FINISHES		77	39.3%	0%	06-Oct-26	06-Dec-26	20-Oct-26	17-Jan-27	35,825.58	0.00	91,162.44	-36
MLTX-02-005-CN-1	Glass Partitions including all accessories and doors	7	0%	0%	01-Nov-26	08-Nov-26	16-Nov-26	23-Nov-26	0.00	0.00	13,649.02	-13
MLTX-02-005-CN-1	Granite Capping for Parpet	2	0%	0%	10-Nov-26	11-Nov-26	06-Dec-26	07-Dec-26	0.00	0.00	8,150.24	-22
MLTX-02-005-CN-1	Painting Finish Works for External Walls	7	100%	0%	06-Oct-26	13-Oct-26	20-Oct-26	27-Oct-26	35,825.58	0.00	35,825.58	-12
MLTX-02-005-CN-1	Phenolic Partitions for Toilets	7	0%	0%	24-Oct-26	31-Oct-26	08-Nov-26	15-Nov-26	0.00	0.00	31,197.60	-13
MLTX-02-005-CN-1	Painting Finish Works for Internal Walls	2	0%	0%	05-Dec-26	06-Dec-26	16-Jan-27	17-Jan-27	0.00	0.00	2,340.00	-36
CELLING FINISHES		80	38.55%	19.28%	12-Oct-26	09-Dec-26	19-Oct-26 A	20-Jan-27	5,771.52	2,885.76	14,970.90	-36
MLTX-02-005-CN-1	Preliminary Works for Ceiling Painting Works	15	0%	0%	15-Nov-26	01-Dec-26	24-Nov-26	10-Dec-26	0.00	0.00	5,771.52	-8
MLTX-02-005-CN-1	Painting Finish Works for Ceiling	3	0%	0%	07-Dec-26	09-Dec-26	18-Jan-27	20-Jan-27	0.00	0.00	3,427.86	-36
MLTX-02-005-CN-1	Gypsum Board Suspended Ceiling Finish Works For Ceiling	7	100%	50%	12-Oct-26	19-Oct-26	19-Oct-26 A	27-Oct-26	5,771.52	2,885.76	5,771.52	-7
SPECIALTIES WORK		76	10%	0%	18-Oct-26	17-Dec-26	02-Nov-26	28-Jan-27	5,849.58	0.00	58,495.83	-36
MLTX-02-005-CN-113	Installation of Phenolic Locker	3	0%	0%	15-Dec-26	17-Dec-26	26-Jan-27	28-Jan-27	0.00	0.00	24,373.26	-36
MLTX-02-005-CN-113	Sanitary Fixtures and Accessories Works	5	40%	0%	18-Oct-26	22-Oct-26	02-Nov-26	07-Nov-26	5,849.58	0.00	14,623.96	-13
MLTX-02-005-CN-114	Installation of MODON Logo on the entrance	3	0%	0%	12-Dec-26	14-Dec-26	23-Jan-27	25-Jan-27	0.00	0.00	19,498.61	-36
TESTING & COMMISSIONING		17	0%	0%	20-Dec-26	02-Jan-27	27-Feb-27	21-Mar-27	0.00	0.00	0.00	-63
MLTX-02-005-TC-11860	Testing and Commissioning for MEP Works for Playground	2	0%	0%	30-Dec-26	31-Dec-26	20-Mar-27	21-Mar-27	0.00	0.00	0.00	-64
MLTX-02-005-TC-11870	Testing and Commissioning for MEP Works for Toilet/Service	12	0%	0%	20-Dec-26	02-Jan-27	27-Feb-27	15-Mar-27	0.00	0.00	0.00	-58
MLTX-02-005-TC-11880	Testing and Commissioning for MEP Works for Landscape	5	0%	0%	27-Dec-26	31-Dec-26	07-Mar-27	15-Mar-27	0.00	0.00	0.00	-59
HASA OASIS		221	9.72%	13%	04-May-26	02-Jan-27	01-Jun-26 A	19-Apr-27	630,832.92	843,797.67	6,491,107.82	-88
ENGINEERING		55	0%	0%	04-May-26	01-Dec-26	20-Oct-26	22-Dec-26	0.00	0.00	0.00	-18
SHOP DRAWINGS		55	0%	0%	04-May-26	01-Dec-26	20-Oct-26	22-Dec-26	0.00	0.00	0.00	-18
SHOP DRAWINGS SUBMISSION		55	0%	0%	04-May-26	01-Dec-26	20-Oct-26	22-Dec-26	0.00	0.00	0.00	-18
SHOP DRAWINGS SUBMITTALS FOR PLAYGROUND WORKS		55	0%	0%	04-May-26	01-Dec-26	20-Oct-26	22-Dec-26	0.00	0.00	0.00	-18
MECHANCAL WORKS		25	0%	0%	26-Sep-26	24-Oct-26	20-Oct-26	17-Nov-26	0.00	0.00	0.00	-21
MLTX-02-005-EM	Shop DWG Submittal for HVAC Plan	25	84%	0%	26-Sep-26	24-Oct-26	20-Oct-26	17-Nov-26	0.00	0.00	0.00	-21
MLTX-02-005-EM	Shop DWG Submittal for Exhaust Air Plan	25	84%	0%	26-Sep-26	24-Oct-26	20-Oct-26	17-Nov-26	0.00	0.00	0.00	-21
ELECTRICAL WORKS		55	0%	0%	04-May-26	01-Dec-26	20-Oct-26	22-Dec-26	0.00	0.00	0.00	-18
MLTX-02-005-EM	Shop DWG Submittal for Lighting Layout	25	84%	0%	26-Sep-26	24-Oct-26	20-Oct-26	17-Nov-26	0.00	0.00	0.00	-21
MLTX-02-005-EM	Shop DWG Submittal for Power Layout	25	100%	0%	04-May-26	04-Jun-26	20-Oct-26	17-Nov-26	0.00	0.00	0.00	-141
MLTX-02-005-EM	Shop DWG Submittal for Power Single Line Diagram	25	72%	0%	29-Sep-26	27-Oct-26	20-Oct-26	17-Nov-26	0.00	0.00	0.00	-18
MLTX-02-005-EM	Shop DWG Submittal for Panel Board Schedules	25	72%	0%	29-Sep-26	27-Oct-26	20-Oct-26	17-Nov-26	0.00	0.00	0.00	-18

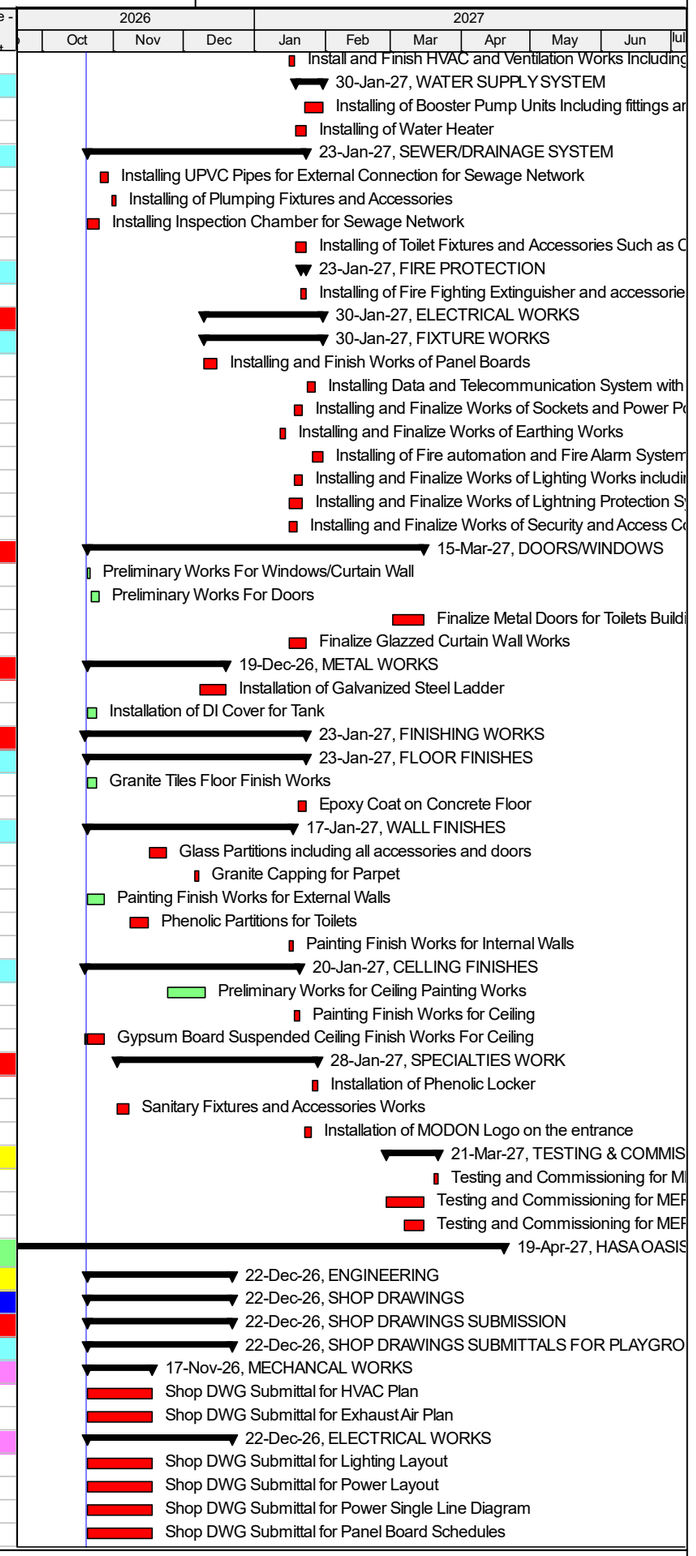

Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary

TASK filter: Remaining works.

© Oracle Corporation

MLTX-02-005 - Playground Initiative for Eastern Region (Arar-Hasa osis -Dammam)


Remaining work
D.D 19-10-2026

PROFAST شركة برو فاست المحدودة

egis

MODON مدن

Activity ID	Activity Name	Original Duration	Schedule % Complete	Performance % Complete	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Variance - BL Project
MLTX-02-005-EI	Shop DWG Submittal for Power Installation Details	25	72%	0%	29-Sep-26	27-Oct-26	20-Oct-26	17-Nov-26	0.00	0.00	0.00	-18
MLTX-02-005-EI	Shop DWG Submittal for Fire Alarm Installation Details	30	0%	0%	25-Oct-26	28-Nov-26	18-Nov-26	22-Dec-26	0.00	0.00	0.00	-21
MLTX-02-005-EI	Shop DWG Submittal for Fire Alarm Layout	30	0%	0%	25-Oct-26	28-Nov-26	18-Nov-26	22-Dec-26	0.00	0.00	0.00	-21
MLTX-02-005-EI	Shop DWG Submittal for Fire Alarm Riser Diagram	30	0%	0%	28-Oct-26	01-Dec-26	18-Nov-26	22-Dec-26	0.00	0.00	0.00	-18
SHOP DRAWINGS APPROVALS		50	0%	0%	06-Jun-26	25-Nov-26	20-Oct-26	16-Dec-26	0.00	0.00	0.00	-18
SHOP DRAWINGS APPROVAL FOR PLAYGROUND WORKS		50	0%	0%	06-Jun-26	25-Nov-26	20-Oct-26	16-Dec-26	0.00	0.00	0.00	-18
SPORTS EQUIPMENT		21	0%	0%	10-Oct-26	02-Nov-26	20-Oct-26	12-Nov-26	0.00	0.00	0.00	-9
MLTX-02-005-EI	Shop DWG Approval for Football Turf Installation	21	42.86%	0%	10-Oct-26	02-Nov-26	20-Oct-26	12-Nov-26	0.00	0.00	0.00	-9
MECHANCAL WORKS		23	0%	0%	25-Oct-26	19-Nov-26	18-Nov-26	14-Dec-26	0.00	0.00	0.00	-21
MLTX-02-005-EI	Shop DWG Approval for HVAC Plan	23	0%	0%	25-Oct-26	19-Nov-26	18-Nov-26	14-Dec-26	0.00	0.00	0.00	-21
MLTX-02-005-EI	Shop DWG Approval for Exhaust Air Plan	23	0%	0%	25-Oct-26	19-Nov-26	18-Nov-26	14-Dec-26	0.00	0.00	0.00	-21
ELECTRICAL WORKS		25	0%	0%	06-Jun-26	25-Nov-26	18-Nov-26	16-Dec-26	0.00	0.00	0.00	-18
MLTX-02-005-EI	Shop DWG Approval for Lighting Layout	25	0%	0%	25-Oct-26	22-Nov-26	18-Nov-26	16-Dec-26	0.00	0.00	0.00	-21
MLTX-02-005-EI	Shop DWG Approval for Power Layout	25	100%	0%	06-Jun-26	04-Jul-26	18-Nov-26	16-Dec-26	0.00	0.00	0.00	-141
MLTX-02-005-EI	Shop DWG Approval for Power Single Line Diagram	25	0%	0%	28-Oct-26	25-Nov-26	18-Nov-26	16-Dec-26	0.00	0.00	0.00	-18
MLTX-02-005-EI	Shop DWG Approval for Panel Board Schedules	25	0%	0%	28-Oct-26	25-Nov-26	18-Nov-26	16-Dec-26	0.00	0.00	0.00	-18
MLTX-02-005-EI	Shop DWG Approval for Power Installation Details	25	0%	0%	28-Oct-26	25-Nov-26	18-Nov-26	16-Dec-26	0.00	0.00	0.00	-18
PROCUREMENT		121	0%	0%	10-Jun-26	01-Dec-26	20-Oct-26	14-Mar-27	0.00	0.00	0.00	-84
SHORT LEAD ITEM		121	0%	0%	16-Jun-26	01-Dec-26	20-Oct-26	14-Mar-27	0.00	0.00	0.00	-84
TOILET/SERVICE WORKS		49	0%	0%	16-Jun-26	19-Oct-26	20-Oct-26	15-Dec-26	0.00	0.00	0.00	-49
LIGHTING FIXTURES		20	0%	0%	16-Jun-26	08-Jul-26	20-Oct-26	11-Nov-26	0.00	0.00	0.00	-107
MLTX-02-005-PR-1	Material Delivery for Lighting Fixtures	20	100%	0%	16-Jun-26	08-Jul-26	20-Oct-26	11-Nov-26	0.00	0.00	0.00	-107
SWITCHES/SOCKETS		32	0%	0%	16-Jun-26	22-Jul-26	20-Oct-26	25-Nov-26	0.00	0.00	0.00	-107
MLTX-02-005-PR-1	PO for Switches/Sockets	15	100%	0%	16-Jun-26	02-Jul-26	20-Oct-26	05-Nov-26	0.00	0.00	0.00	-107
MLTX-02-005-PR-1	Material Delivery for Switches/Sockets	17	100%	0%	04-Jul-26	22-Jul-26	07-Nov-26	25-Nov-26	0.00	0.00	0.00	-107
DISTRIBUTION PANNELS		20	0%	0%	27-Sep-26	19-Oct-26	20-Oct-26	11-Nov-26	0.00	0.00	0.00	-20
MLTX-02-005-PR-1	PO for Distribution Panels	5	100%	0%	27-Sep-26	01-Oct-26	20-Oct-26	25-Oct-26	0.00	0.00	0.00	-20
MLTX-02-005-PR-1	Material Delivery for Distribution Panels	15	100%	0%	03-Oct-26	19-Oct-26	26-Oct-26	11-Nov-26	0.00	0.00	0.00	-20
FURNITURES		49	0%	0%	16-Jun-26	11-Aug-26	20-Oct-26	15-Dec-26	0.00	0.00	0.00	-107
MLTX-02-005-PR-1	PO for Furnitures	19	100%	0%	16-Jun-26	07-Jul-26	20-Oct-26	10-Nov-26	0.00	0.00	0.00	-107
MLTX-02-005-PR-1	Material Delivery for Furnitures	30	100%	0%	08-Jul-26	11-Aug-26	11-Nov-26	15-Dec-26	0.00	0.00	0.00	-107
PLAYGROUND WORKS		121	0%	0%	28-Jun-26	01-Dec-26	20-Oct-26	14-Mar-27	0.00	0.00	0.00	-84
PVC MEMBRANE		30	0%	0%	29-Sep-26	02-Nov-26	07-Nov-26	10-Dec-26	0.00	0.00	0.00	-33
MLTX-02-005-PR-1	Material Delivery for PVC Membrane	30	60%	0%	29-Sep-26	02-Nov-26	07-Nov-26	10-Dec-26	0.00	0.00	0.00	-33
ARTIFICIAL TURF		30	0%	0%	30-Sep-26	03-Nov-26	20-Oct-26	23-Nov-26	0.00	0.00	0.00	-17
MLTX-02-005-PR-1	Material Delivery for Artificial TURF	30	56.67%	0%	30-Sep-26	03-Nov-26	20-Oct-26	23-Nov-26	0.00	0.00	0.00	-17
RUBBER GRANULES		30	0%	0%	20-Sep-26	25-Oct-26	20-Oct-26	23-Nov-26	0.00	0.00	0.00	-25
MLTX-02-005-PR-1	Material Delivery for Rubber Granules	30	83.33%	0%	20-Sep-26	25-Oct-26	20-Oct-26	23-Nov-26	0.00	0.00	0.00	-25
PADEL GLASS		30	0%	0%	16-Sep-26	21-Oct-26	20-Oct-26	23-Nov-26	0.00	0.00	0.00	-28
MLTX-02-005-PR-1	Material Delivery for Padel Glass	30	93.33%	0%	16-Sep-26	21-Oct-26	20-Oct-26	23-Nov-26	0.00	0.00	0.00	-28
PADEL WIRE MESH/STEEL SETS		15	0%	0%	16-Sep-26	04-Oct-26	20-Oct-26	05-Nov-26	0.00	0.00	0.00	-28
MLTX-02-005-PR-1	Material Delivery for Wire Mesh/Steel Sets	15	100%	0%	16-Sep-26	04-Oct-26	20-Oct-26	05-Nov-26	0.00	0.00	0.00	-28
MARKING PAINT		32	0%	0%	28-Jun-26	03-Aug-26	20-Oct-26	25-Nov-26	0.00	0.00	0.00	-97
MLTX-02-005-PR-1	PO for Marking Paint	15	100%	0%	28-Jun-26	14-Jul-26	20-Oct-26	05-Nov-26	0.00	0.00	0.00	-97
MLTX-02-005-PR-1	Material Delivery for Marking Paint	17	100%	0%	15-Jul-26	03-Aug-26	07-Nov-26	25-Nov-26	0.00	0.00	0.00	-97
AIR DIFUSSERS/GRILLS		40	0%	0%	24-Sep-26	09-Nov-26	20-Oct-26	05-Dec-26	0.00	0.00	0.00	-22
MLTX-02-005-PR-1	PO for Air Difussers/Grills	15	100%	0%	24-Sep-26	11-Oct-26	20-Oct-26	05-Nov-26	0.00	0.00	0.00	-22
MLTX-02-005-PR-1	Material Delivery for Air Difussers/Grills	25	28%	0%	12-Oct-26	09-Nov-26	07-Nov-26	05-Dec-26	0.00	0.00	0.00	-22
GALVANIZED DUCTS		40	0%	0%	24-Sep-26	09-Nov-26	20-Oct-26	05-Dec-26	0.00	0.00	0.00	-22
MLTX-02-005-PR-1	PO for Galvanized Duct	15	100%	0%	24-Sep-26	11-Oct-26	20-Oct-26	05-Nov-26	0.00	0.00	0.00	-22
MLTX-02-005-PR-1	Material Delivery for Galvanized Duct	25	28%	0%	12-Oct-26	09-Nov-26	07-Nov-26	05-Dec-26	0.00	0.00	0.00	-22
EXHAUST FANS		40	0%	0%	10-Sep-26	02-Nov-26	20-Oct-26	05-Dec-26	0.00	0.00	0.00	-28
MLTX-02-005-PR-1	PO for Exhaust Fans	15	100%	0%	10-Sep-26	28-Sep-26	20-Oct-26	05-Nov-26	0.00	0.00	0.00	-33
MLTX-02-005-PR-1	Material Delivery for Exhaust Fans	25	52%	0%	05-Oct-26	02-Nov-26	07-Nov-26	05-Dec-26	0.00	0.00	0.00	-28
DISTRIBUTION BOARDS		20	0%	0%	10-Oct-26	01-Nov-26	07-Nov-26	29-Nov-26	0.00	0.00	0.00	-24
MLTX-02-005-PR-1	PO for Distribution Boards	5	100%	0%	10-Oct-26	14-Oct-26	07-Nov-26	11-Nov-26	0.00	0.00	0.00	-24
MLTX-02-005-PR-1	Material Delivery for Distribution Boards	15	26.67%	0%	15-Oct-26	01-Nov-26	12-Nov-26	29-Nov-26	0.00	0.00	0.00	-24
POWER CABLES		35	0%	0%	22-Oct-26	01-Dec-26	24-Nov-26	03-Jan-27	0.00	0.00	0.00	-28
MLTX-02-005-PR-1	PO for Power Cables	15	0%	0%	22-Oct-26	08-Nov-26	24-Nov-26	10-Dec-26	0.00	0.00	0.00	-28
MLTX-02-005-PR-1	Material Delivery for Power Cables	20	0%	0%	09-Nov-26	01-Dec-26	12-Dec-26	03-Jan-27	0.00	0.00	0.00	-28
LIGHT FIXTURES		20	0%	0%	09-Nov-26	01-Dec-26	15-Feb-27	14-Mar-27	0.00	0.00	0.00	-84
MLTX-02-005-PR-1	Material Delivery for Light Fixtures	20	0%	0%	09-Nov-26	01-Dec-26	15-Feb-27	14-Mar-27	0.00	0.00	0.00	-84
CCTV MATERIALS		88	0%	0%	04-Jul-26	29-Nov-26	20-Oct-26	30-Jan-27	0.00	0.00	0.00	-53
MLTX-02-005-PR-1	PO for CCTV	15	100%	0%	04-Jul-26	20-Jul-26	20-Oct-26	05-Nov-26	0.00	0.00	0.00	-92

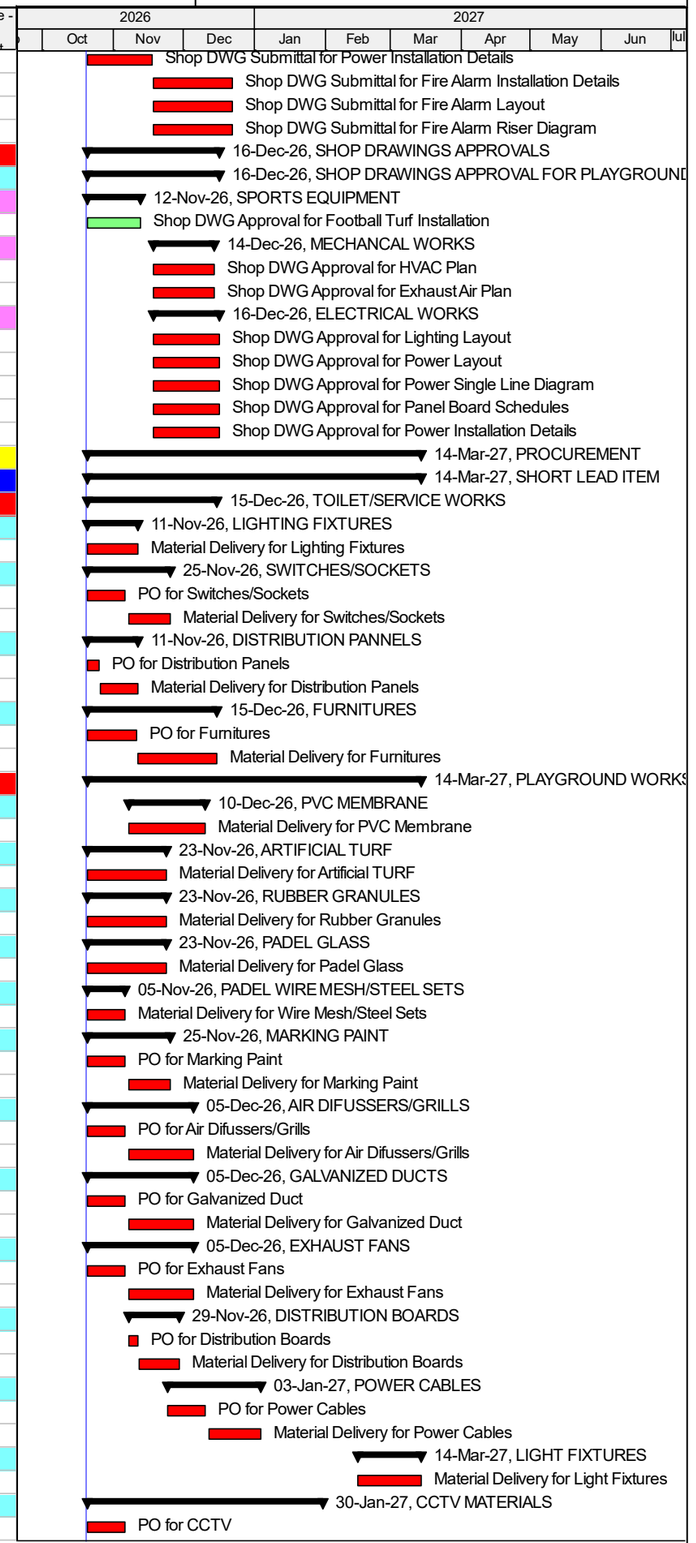

Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary


TASK filter: Remaining works.

© Oracle Corporation

MLTX-02-005 - Playground Initiative for Eastern Region (Arar-Hasa osis -Dammam)

Remaining work
D.D 19-10-2026

Activity ID	Activity Name	Original Duration	Schedule % Complete	Performance % Complete	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Variance - BL Project
MLTX-02-005-PR-1	Material Delivery for CCTV	15	0%	0%	12-Nov-26	29-Nov-26	13-Jan-27	30-Jan-27	0.00	0.00	0.00	-53
POWER OUTLETS/SWITCHES		41	0%	0%	23-Jul-26	10-Nov-26	26-Nov-26	12-Jan-27	0.00	0.00	0.00	-54
MLTX-02-005-PR-1	PO for Power Outlets/Switches	16	100%	0%	23-Jul-26	10-Aug-26	26-Nov-26	14-Dec-26	0.00	0.00	0.00	-107
MLTX-02-005-PR-1	Material Delivery for Power Outlets/Switches	25	24%	0%	13-Oct-26	10-Nov-26	15-Dec-26	12-Jan-27	0.00	0.00	0.00	-54
LANDSCAPE WORKS		53	0%	0%	11-Aug-26	04-Nov-26	15-Dec-26	14-Feb-27	0.00	0.00	0.00	-87
PAVEMENT MARKING		33	0%	0%	11-Aug-26	04-Nov-26	15-Dec-26	21-Jan-27	0.00	0.00	0.00	-67
MLTX-02-005-PR-1	PO for Pavement Markings	13	100%	0%	11-Aug-26	25-Aug-26	15-Dec-26	29-Dec-26	0.00	0.00	0.00	-107
MLTX-02-005-PR-1	Material Delivery for Pavement Markings	20	30%	0%	13-Oct-26	04-Nov-26	30-Dec-26	21-Jan-27	0.00	0.00	0.00	-67
TRAFFIC SIGNS		20	0%	0%	03-Sep-26	27-Sep-26	30-Dec-26	21-Jan-27	0.00	0.00	0.00	-100
MLTX-02-005-PR-1	PO for Traffic Signs	15	100%	0%	03-Sep-26	20-Sep-26	30-Dec-26	16-Jan-27	0.00	0.00	0.00	-100
MLTX-02-005-PR-1	Material Delivery for Traffic Signs	5	100%	0%	21-Sep-26	27-Sep-26	17-Jan-27	21-Jan-27	0.00	0.00	0.00	-100
TRACK SURFACE		2	0%	0%	29-Aug-26	30-Aug-26	30-Dec-26	31-Dec-26	0.00	0.00	0.00	-105
MLTX-02-005-PR-1	Material Delivery for Track Surface	2	100%	0%	29-Aug-26	30-Aug-26	30-Dec-26	31-Dec-26	0.00	0.00	0.00	-105
GRASS/TREES		25	0%	0%	28-Sep-26	26-Oct-26	17-Jan-27	14-Feb-27	0.00	0.00	0.00	-95
MLTX-02-005-PR-1	Material Delivery for Grass/Trees	25	76%	0%	28-Sep-26	26-Oct-26	17-Jan-27	14-Feb-27	0.00	0.00	0.00	-95
LONG LEAD ITEM		119	0%	0%	10-Jun-26	16-Nov-26	20-Oct-26	08-Mar-27	0.00	0.00	0.00	-95
PLAYGROUND WORKS		119	0%	0%	10-Jun-26	16-Nov-26	20-Oct-26	08-Mar-27	0.00	0.00	0.00	-95
STEEL TENSION CABLES		43	0%	0%	01-Sep-26	21-Oct-26	28-Dec-26	15-Feb-27	0.00	0.00	0.00	-100
MLTX-02-005-PR-1	PO for Steel Tension Cables	7	100%	0%	01-Sep-26	08-Sep-26	28-Dec-26	04-Jan-27	0.00	0.00	0.00	-100
MLTX-02-005-PR-1	Material Delivery for Steel Tension Cables	16	100%	0%	21-Sep-26	10-Oct-26	17-Jan-27	03-Feb-27	0.00	0.00	0.00	-100
MLTX-02-005-PR-1	Material Fabrication for Steel Tension Cables	10	100%	0%	09-Sep-26	20-Sep-26	05-Jan-27	16-Jan-27	0.00	0.00	0.00	-100
MLTX-02-005-PR-1	Staging time	10	80%	0%	11-Oct-26	21-Oct-26	04-Feb-27	15-Feb-27	0.00	0.00	0.00	-100
EMERGENCY DOORS		60	0%	0%	10-Jun-26	18-Aug-26	20-Oct-26	28-Dec-26	0.00	0.00	0.00	-112
MLTX-02-005-PR-1	PO for Emergency Doors	10	100%	0%	10-Jun-26	21-Jun-26	20-Oct-26	31-Oct-26	0.00	0.00	0.00	-112
MLTX-02-005-PR-1	Material Delivery for Emergency Doors	25	100%	0%	15-Jul-26	12-Aug-26	24-Nov-26	22-Dec-26	0.00	0.00	0.00	-112
MLTX-02-005-PR-1	Material Fabrication for Emergency Doors	20	100%	0%	22-Jun-26	14-Jul-26	01-Nov-26	23-Nov-26	0.00	0.00	0.00	-112
MLTX-02-005-PR-1	Staging time	5	100%	0%	13-Aug-26	18-Aug-26	23-Dec-26	28-Dec-26	0.00	0.00	0.00	-112
PRESSURE UNITS		60	0%	0%	07-Sep-26	16-Nov-26	28-Dec-26	08-Mar-27	0.00	0.00	0.00	-95
MLTX-02-005-PR-1	PO for Pressure Units	10	100%	0%	07-Sep-26	17-Sep-26	28-Dec-26	07-Jan-27	0.00	0.00	0.00	-95
MLTX-02-005-PR-1	Material Delivery for Pressure Units	25	24%	0%	13-Oct-26	10-Nov-26	01-Feb-27	02-Mar-27	0.00	0.00	0.00	-95
MLTX-02-005-PR-1	Material Fabrication for Pressure Units	20	100%	0%	19-Sep-26	12-Oct-26	09-Jan-27	31-Jan-27	0.00	0.00	0.00	-95
MLTX-02-005-PR-1	Staging time	5	0%	0%	11-Nov-26	16-Nov-26	03-Mar-27	08-Mar-27	0.00	0.00	0.00	-95
AIR LOCK DOORS		60	0%	0%	20-Aug-26	05-Nov-26	16-Dec-26	24-Feb-27	0.00	0.00	0.00	-94
MLTX-02-005-PR-1	PO for Lock Doors	10	100%	0%	20-Aug-26	31-Aug-26	16-Dec-26	27-Dec-26	0.00	0.00	0.00	-100
MLTX-02-005-PR-1	Material Delivery for Lock Doors	25	60%	0%	03-Oct-26	31-Oct-26	20-Jan-27	17-Feb-27	0.00	0.00	0.00	-94
MLTX-02-005-PR-1	Material Fabrication for Lock Doors	20	100%	0%	08-Sep-26	01-Oct-26	28-Dec-26	19-Jan-27	0.00	0.00	0.00	-94
MLTX-02-005-PR-1	Staging time	5	0%	0%	01-Nov-26	05-Nov-26	18-Feb-27	24-Feb-27	0.00	0.00	0.00	-94
CONSTRUCTION PHASE		219	9.72%	13%	30-Jul-26	31-Dec-26	01-Jun-26 A	17-Apr-27	630,832.92	843,797.67	6,491,107.82	-87
SITE WORKS		168	9.23%	12.91%	29-Sep-26	31-Dec-26	01-Jun-26 A	17-Apr-27	561,021.73	784,908.93	6,077,960.83	-87
LANDSCAPE WORKS		168	9.23%	12.91%	29-Sep-26	31-Dec-26	01-Jun-26 A	17-Apr-27	561,021.73	784,908.93	6,077,960.83	-87
PLAYGROUND AREA		168	40.56%	28.39%	29-Sep-26	31-Dec-26	21-Sep-26 A	17-Apr-27	180,520.67	126,364.47	445,050.38	-87
FOOTBALL PLAYGROUND		77	0%	0%	17-Nov-26	09-Dec-26	22-Nov-26	18-Feb-27	0.00	0.00	47,527.50	-61
MLTX-02-005-CI	Install Sport Equipments - Goal / Nets - (Football Playground)	20	0%	0%	17-Nov-26	09-Dec-26	22-Nov-26	14-Dec-26	0.00	0.00	31,685.00	-4
MLTX-02-005-CI	Surface Marking and Painting (Football Playground)	3	0%	0%	17-Nov-26	19-Nov-26	16-Feb-27	18-Feb-27	0.00	0.00	15,842.50	-78
PADEL PLAYGROUND		18	0%	0%	12-Dec-26	31-Dec-26	20-Feb-27	16-Mar-27	0.00	0.00	70,195.20	-60
MLTX-02-005-CI	Install Sport Equipments - Goal / Nets - (Padel Playground)	15	0%	0%	12-Dec-26	28-Dec-26	20-Feb-27	09-Mar-27	0.00	0.00	58,496.00	-60
MLTX-02-005-CI	Surface Marking and Painting (Padel Playground)	3	0%	0%	29-Dec-26	31-Dec-26	14-Mar-27	16-Mar-27	0.00	0.00	11,699.20	-60
BASKETBALL PLAYGROUND		95	0%	0%	17-Nov-26	31-Dec-26	22-Nov-26	16-Mar-27	0.00	0.00	96,956.10	-60
MLTX-02-005-CI	Install Sport Equipments - Goal / Nets - (Basketball	10	0%	0%	17-Nov-26	28-Nov-26	22-Nov-26	02-Dec-26	0.00	0.00	80,796.75	-4
MLTX-02-005-CI	Surface Marking and Painting (Basketball Playground)	3	0%	0%	29-Dec-26	31-Dec-26	14-Mar-27	16-Mar-27	0.00	0.00	16,159.35	-60
PADEL FENCE		45	0%	0%	02-Dec-26	31-Dec-26	20-Feb-27	17-Apr-27	0.00	0.00	49,850.91	-87
MLTX-02-005-CI	Tempered Glass Fenc Installation and Fixation	15	0%	0%	02-Dec-26	19-Dec-26	20-Feb-27	09-Mar-27	0.00	0.00	30,677.48	-68
MLTX-02-005-CI	Chain Link Fence Installation and Fixation	15	0%	0%	02-Dec-26	19-Dec-26	20-Feb-27	09-Mar-27	0.00	0.00	15,338.75	-68
MLTX-02-005-CI	Install of Fence Gates	26	0%	0%	02-Dec-26	31-Dec-26	18-Mar-27	17-Apr-27	0.00	0.00	3,834.68	-87
CURBSTOEN/INTERLOCK		3	100%	70%	29-Sep-26	01-Oct-26	21-Sep-26 A	22-Oct-26	180,520.67	126,364.47	180,520.67	-18
MLTX-02-005-CI	Interlock Installation (Grey Scale) for LandScape (Including	3	100%	70%	29-Sep-26	01-Oct-26	21-Sep-26 A	22-Oct-26	180,520.67	126,364.47	180,520.67	-18
AIR DOME		32	0%	0%	15-Nov-26	10-Dec-26	16-Feb-27	29-Mar-27	0.00	0.00	4,306,367.09	-89
CIVIL WORKS		20	0%	0%	15-Nov-26	07-Dec-26	16-Feb-27	15-Mar-27	0.00	0.00	1,391,301.90	-80
MLTX-02-005-CI	Install of Membrane Covering System (Air Dome)	20	0%	0%	15-Nov-26	07-Dec-26	16-Feb-27	15-Mar-27	0.00	0.00	942,830.33	-80
MLTX-02-005-CI	Thermal Insulation Works (Air Dome)	20	0%	0%	15-Nov-26	07-Dec-26	16-Feb-27	15-Mar-27	0.00	0.00	448,471.57	-80
MECHANICAL WORKS		15	0%	0%	21-Nov-26	07-Dec-26	09-Mar-27	29-Mar-27	0.00	0.00	1,233,296.81	-92
MLTX-02-005-CI	Air Ducts and Grills Installation (Air Dome)	15	0%	0%	21-Nov-26	07-Dec-26	09-Mar-27	29-Mar-27	0.00	0.00	728,766.30	-92
MLTX-02-005-CI	Air Units Installation (Air Dome)	8	0%	0%	29-Nov-26	07-Dec-26	21-Mar-27	29-Mar-27	0.00	0.00	336,353.67	-92
MLTX-02-005-CI	Exhaust Fans and Ducts Installation (Air Dome)	8	0%	0%	29-Nov-26	07-Dec-26	21-Mar-27	29-Mar-27	0.00	0.00	168,176.84	-92

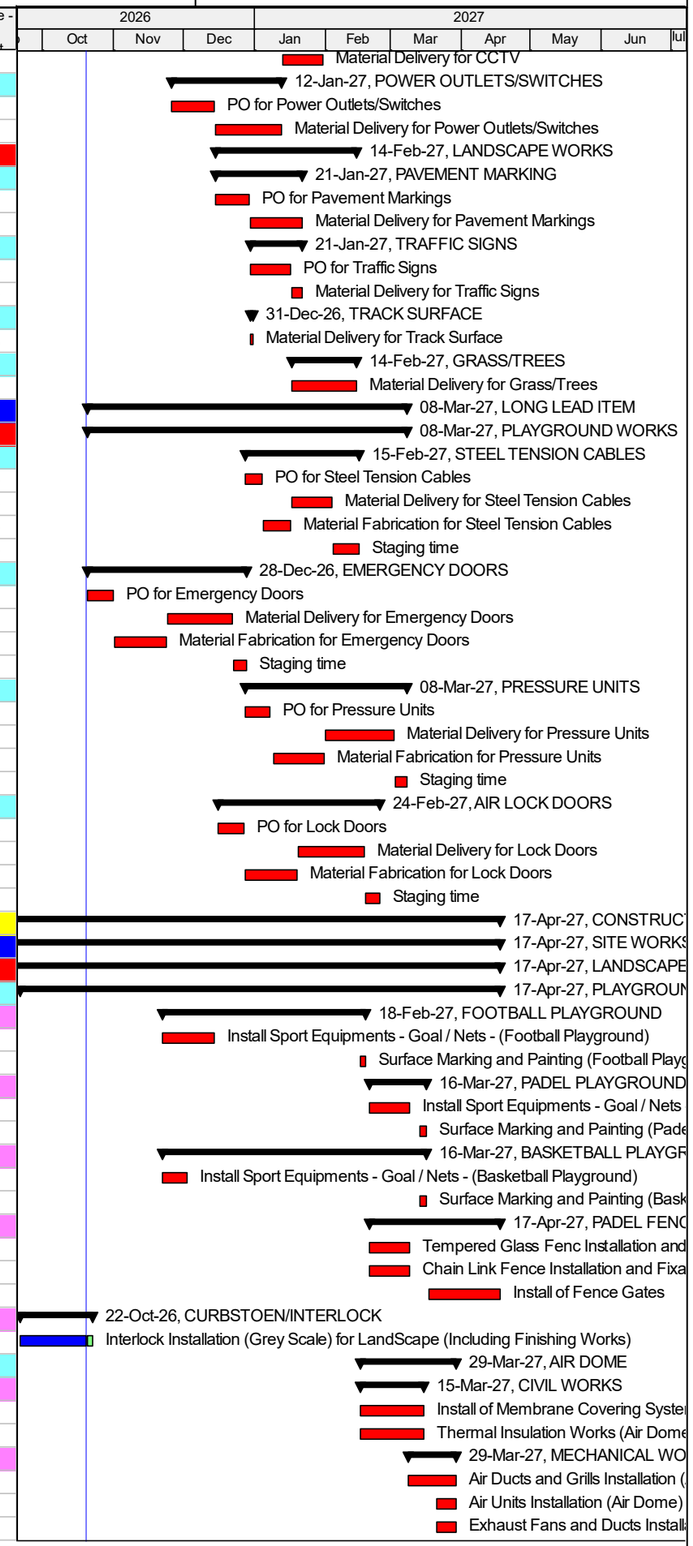

Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary


TASK filter: Remaining works.

© Oracle Corporation

MLTX-02-005 - Playground Initiative for Eastern Region (Arar-Hasa osis -Dammam)

Remaining work
D.D 19-10-2026

Activity ID	Activity Name	Original Duration	Schedule % Complete	Performance % Complete	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Variance - BL Project
ELECTRICAL WORKS		8	0%	0%	02-Dec-26	10-Dec-26	21-Mar-27	29-Mar-27	0.00	0.00	1,513,591.54	-89
MLTX-02-005-CI	Light Fixture Works (Air Dome)	8	0%	0%	02-Dec-26	10-Dec-26	21-Mar-27	29-Mar-27	0.00	0.00	224,235.78	-89
MLTX-02-005-CI	Distribution Board and Electrical Works (Air Dome)	8	0%	0%	02-Dec-26	10-Dec-26	21-Mar-27	29-Mar-27	0.00	0.00	168,176.84	-89
MLTX-02-005-CI	External Electrical Connection Works (Air Dome)	8	0%	0%	02-Dec-26	10-Dec-26	21-Mar-27	29-Mar-27	0.00	0.00	168,176.84	-89
MLTX-02-005-CI	Emergency Generator Installation (Air Dome)	8	0%	0%	02-Dec-26	10-Dec-26	21-Mar-27	29-Mar-27	0.00	0.00	504,530.51	-89
MLTX-02-005-CI	Control System Installation (Air Dome)	8	0%	0%	02-Dec-26	10-Dec-26	21-Mar-27	29-Mar-27	0.00	0.00	448,471.57	-89
FINISHES WORKS		25	0%	0%	15-Nov-26	10-Dec-26	25-Feb-27	29-Mar-27	0.00	0.00	168,176.84	-89
MLTX-02-005-CI	Doors Installation Including Emergency, Entrance doors (Air	15	0%	0%	15-Nov-26	01-Dec-26	25-Feb-27	17-Mar-27	0.00	0.00	112,117.89	-87
MLTX-02-005-CI	Logo and Signs Installation (Air Dome)	2	0%	0%	09-Dec-26	10-Dec-26	28-Mar-27	29-Mar-27	0.00	0.00	56,058.95	-89
IRRIGATION NETWORK		3	0%	0%	05-Dec-26	07-Dec-26	07-Mar-27	09-Mar-27	0.00	0.00	25,106.20	-78
MLTX-02-005-CN-1	Installing of Bubblers and Spreyers	3	0%	0%	05-Dec-26	07-Dec-26	07-Mar-27	09-Mar-27	0.00	0.00	25,106.20	-78
NATURAL GROUND		15	0%	53.56%	29-Nov-26	07-Dec-26	13-Oct-26 A	25-Oct-26	0.00	102,696.00	191,740.00	37
MLTX-02-005-CN-1	Tartan Floor Installation Works for Landscape (Including	3	0%	40%	05-Dec-26	07-Dec-26	14-Oct-26 A	22-Oct-26	0.00	50,696.00	126,740.00	39
MLTX-02-005-CN-1	Compacted Natural Ground Soil Installation Works for	5	0%	80%	29-Nov-26	03-Dec-26	13-Oct-26 A	25-Oct-26	0.00	52,000.00	65,000.00	34
PLANTING		101	0%	42%	24-Oct-26	02-Nov-26	03-Oct-26 A	22-Oct-26	0.00	145,845.61	347,251.46	9
MLTX-02-005-CN-1	Placement of Sweet/Agricultural Soil (Including Levelling and	3	0%	70%	24-Oct-26	26-Oct-26	03-Oct-26 A	22-Oct-26	0.00	72,922.81	104,175.44	3
MLTX-02-005-CN-1	Placement of Lawn Ground Cover (Rolling and Compaction)	3	0%	30%	31-Oct-26	02-Nov-26	14-Oct-26 A	22-Oct-26	0.00	42,519.75	141,732.50	9
MLTX-02-005-CN-1	Placement and Fixation of Trees	3	0%	30%	27-Oct-26	29-Oct-26	14-Oct-26 A	22-Oct-26	0.00	30,403.06	101,343.52	6
WALKING/BIKE PATHS		16	100%	75%	29-Sep-26	17-Oct-26	01-Jun-26 A	20-Oct-26	367,633.90	275,725.43	367,633.90	-2
MLTX-02-005-CN-1	Bike Path Preparation and Installation Works	8	100%	75%	29-Sep-26	07-Oct-26	01-Jun-26 A	20-Oct-26	187,554.12	140,665.59	187,554.12	-10
MLTX-02-005-CN-1	Walking Path Preparation and Installation Works	8	100%	75%	08-Oct-26	17-Oct-26	10-Jun-26 A	20-Oct-26	180,079.78	135,059.83	180,079.78	-2
GENERAL/FURNITURE		130	3.26%	34.01%	15-Oct-26	24-Dec-26	01-Oct-26 A	21-Mar-27	12,867.16	134,277.42	394,811.80	-70
MLTX-02-005-CN-1	Stamped Concrete Works for LandScape (Including	18	11.11%	40%	18-Oct-26	07-Nov-26	14-Oct-26 A	09-Nov-26	10,399.33	37,437.60	93,594.00	-2
MLTX-02-005-CN-1	Traffic Signs Posts and Poles Installation	3	0%	0%	20-Dec-26	22-Dec-26	16-Mar-27	18-Mar-27	0.00	0.00	9,749.30	-70
MLTX-02-005-CN-1	Fixation and Installation of Steel Frame for Benches	28	14.29%	0%	15-Oct-26	16-Nov-26	20-Oct-26	21-Nov-26	2,467.83	0.00	17,274.79	-4
MLTX-02-005-CN-1	Fixation and Installation of Benches	14	0%	0%	17-Nov-26	02-Dec-26	22-Nov-26	07-Dec-26	0.00	0.00	40,307.84	-4
MLTX-02-005-CN-1	Fixation and Installation of Precast Concrete Seats	14	0%	0%	03-Dec-26	19-Dec-26	22-Nov-26	07-Dec-26	0.00	0.00	32,757.76	10
MLTX-02-005-CN-1	Fixation and Installation of Precast Concrete Seats (Circular)	14	0%	0%	03-Dec-26	19-Dec-26	08-Dec-26	23-Dec-26	0.00	0.00	12,869.04	-4
MLTX-02-005-CN-1	Fixation and Installation of Precast Concrete Trash Bins	2	0%	0%	23-Dec-26	24-Dec-26	20-Mar-27	21-Mar-27	0.00	0.00	12,186.67	-70
MLTX-02-005-CN-1	Installing of Site Light Poles	22	0%	55%	08-Nov-26	02-Dec-26	01-Oct-26 A	14-Nov-26	0.00	96,839.82	176,072.40	16
TOILET/SERVICE BUILDING		203	16.9%	14.25%	30-Jul-26	23-Dec-26	20-Sep-26 A	29-Mar-27	69,811.19	58,888.74	413,146.99	-78
THERMAL & MOISTER PROTECTION		18	100%	90%	30-Jul-26	19-Aug-26	20-Sep-26 A	09-Nov-26	16,607.28	14,946.55	16,607.28	-69
MLTX-02-005-CN-126	Finalize Water Proofing Works for Roofing and Wet Areas	18	100%	90%	30-Jul-26	19-Aug-26	20-Sep-26 A	09-Nov-26	16,607.28	14,946.55	16,607.28	-69
MECHANICAL WORK		21	0%	0%	28-Nov-26	21-Dec-26	16-Feb-27	16-Mar-27	0.00	0.00	1,949.87	-69
FIRE PROTECTION		21	0%	0%	28-Nov-26	21-Dec-26	16-Feb-27	16-Mar-27	0.00	0.00	1,949.87	-69
MLTX-02-005-CN-1	Installing of Fire Fighting Extinguisher and accessories	21	0%	0%	28-Nov-26	21-Dec-26	16-Feb-27	16-Mar-27	0.00	0.00	1,949.87	-69
ELECTRICAL WORKS		79	0%	0%	04-Nov-26	21-Dec-26	13-Dec-26	18-Mar-27	0.00	0.00	180,781.27	-71
FIXTURE WORKS		79	0%	0%	04-Nov-26	21-Dec-26	13-Dec-26	18-Mar-27	0.00	0.00	180,781.27	-71
MLTX-02-005-CN-1	Installing of Fire automation and Fire Alarm System	18	0%	0%	28-Nov-26	17-Dec-26	05-Jan-27	25-Jan-27	0.00	0.00	34,317.53	-33
MLTX-02-005-CN-1	Installing and Finish Works of Panel Boards	20	0%	0%	04-Nov-26	26-Nov-26	13-Dec-26	04-Jan-27	0.00	0.00	102,367.69	-33
MLTX-02-005-CN-1	Installing and Finalize Works of Sockets and Power Points	20	0%	0%	28-Nov-26	20-Dec-26	05-Jan-27	27-Jan-27	0.00	0.00	7,085.10	-33
MLTX-02-005-CN-1	Installing and Finalize Works of Lighting Works including Light	21	0%	0%	28-Nov-26	21-Dec-26	05-Jan-27	28-Jan-27	0.00	0.00	14,259.43	-33
MLTX-02-005-CN-1	Installing Data and Telecommunication System with all	20	0%	0%	28-Nov-26	20-Dec-26	05-Jan-27	27-Jan-27	0.00	0.00	6,239.59	-33
MLTX-02-005-CN-1	Installing and Finalize Works of Security and Access Control	20	0%	0%	21-Nov-26	13-Dec-26	20-Feb-27	18-Mar-27	0.00	0.00	7,250.09	-78
MLTX-02-005-CN-1	Installing and Finalize Works of Earthing Works	20	0%	0%	28-Nov-26	20-Dec-26	05-Jan-27	27-Jan-27	0.00	0.00	6,824.51	-33
MLTX-02-005-CN-1	Installing and Finalize Works of Lightning Protection System	20	0%	0%	21-Nov-26	13-Dec-26	20-Feb-27	18-Mar-27	0.00	0.00	2,437.33	-78
DOORS/WINDOWS		23	0%	0%	21-Nov-26	16-Dec-26	20-Feb-27	22-Mar-27	0.00	0.00	58,495.82	-78
MLTX-02-005-CN-130	Finalize Glazzed Curtain Wall Works	11	0%	0%	05-Dec-26	16-Dec-26	07-Mar-27	22-Mar-27	0.00	0.00	5,849.58	-78
MLTX-02-005-CN-131	Preliminary Works For Windows/Curtain Wall	12	0%	0%	21-Nov-26	03-Dec-26	20-Feb-27	06-Mar-27	0.00	0.00	52,646.24	-78
METAL WORKS		14	92.86%	0%	05-Oct-26	20-Oct-26	12-Nov-26	28-Nov-26	3,621.17	0.00	3,899.72	-33
MLTX-02-005-CN-129	Installation of DI Cover for Tank	14	92.86%	0%	05-Oct-26	20-Oct-26	12-Nov-26	28-Nov-26	3,621.17	0.00	3,899.72	-33
FINISHING WORKS		130	37.62%	34.7%	20-Aug-26	16-Dec-26	27-Sep-26 A	22-Mar-27	34,958.78	32,243.02	92,917.20	-78
FLOOR FINISHES		128	71.43%	0%	27-Sep-26	16-Dec-26	20-Oct-26	22-Mar-27	2,924.82	0.00	4,094.76	-78
MLTX-02-005-CN-1	Granite Tiles Floor Finish Works	6	100%	0%	27-Sep-26	03-Oct-26	20-Oct-26	26-Oct-26	2,924.82	0.00	2,924.82	-20
MLTX-02-005-CN-1	Epoxy Coat on Concrete Floor	23	0%	0%	21-Nov-26	16-Dec-26	20-Feb-27	22-Mar-27	0.00	0.00	1,169.94	-78
WALL FINISHES		48	36.07%	36.3%	20-Aug-26	03-Nov-26	27-Sep-26 A	12-Dec-26	32,033.96	32,243.02	88,822.44	-33
MLTX-02-005-CN-1	Painting Finish Works for External Walls	3	66.67%	90%	18-Oct-26	20-Oct-26	27-Sep-26 A	22-Oct-26	23,883.72	32,243.02	35,825.58	-2
MLTX-02-005-CN-1	Phenolic Partitions for Toilets	7	0%	0%	21-Oct-26	28-Oct-26	29-Nov-26	06-Dec-26	0.00	0.00	31,197.60	-33
MLTX-02-005-CN-1	Glass Partitions including all accessories and doors	5	0%	0%	29-Oct-26	03-Nov-26	07-Dec-26	12-Dec-26	0.00	0.00	13,649.02	-33
MLTX-02-005-CN-1	Granite Capping for Parpet	12	100%	0%	20-Aug-26	02-Sep-26	10-Nov-26	23-Nov-26	8,150.24	0.00	8,150.24	-69
SPECIALTIES WORK		154	25%	20%	27-Sep-26	23-Dec-26	04-Oct-26 A	29-Mar-27	14,623.96	11,699.17	58,495.83	-78
MLTX-02-005-CN-127	Sanitary Fixtures and Accessories Works	3	100%	80%	27-Sep-26	29-Sep-26	04-Oct-26 A	22-Oct-26	14,623.96	11,699.17	14,623.96	-20
MLTX-02-005-CN-127	Installation of MODON Logo on the entrance	17	0%	0%	05-Dec-26	23-Dec-26	07-Mar-27	29-Mar-27	0.00	0.00	19,498.61	-78
MLTX-02-005-CN-131	Installation of Phenolic Locker	12	0%	0%	28-Nov-26	10-Dec-26	05-Jan-27	18-Jan-27	0.00	0.00	24,373.26	-33

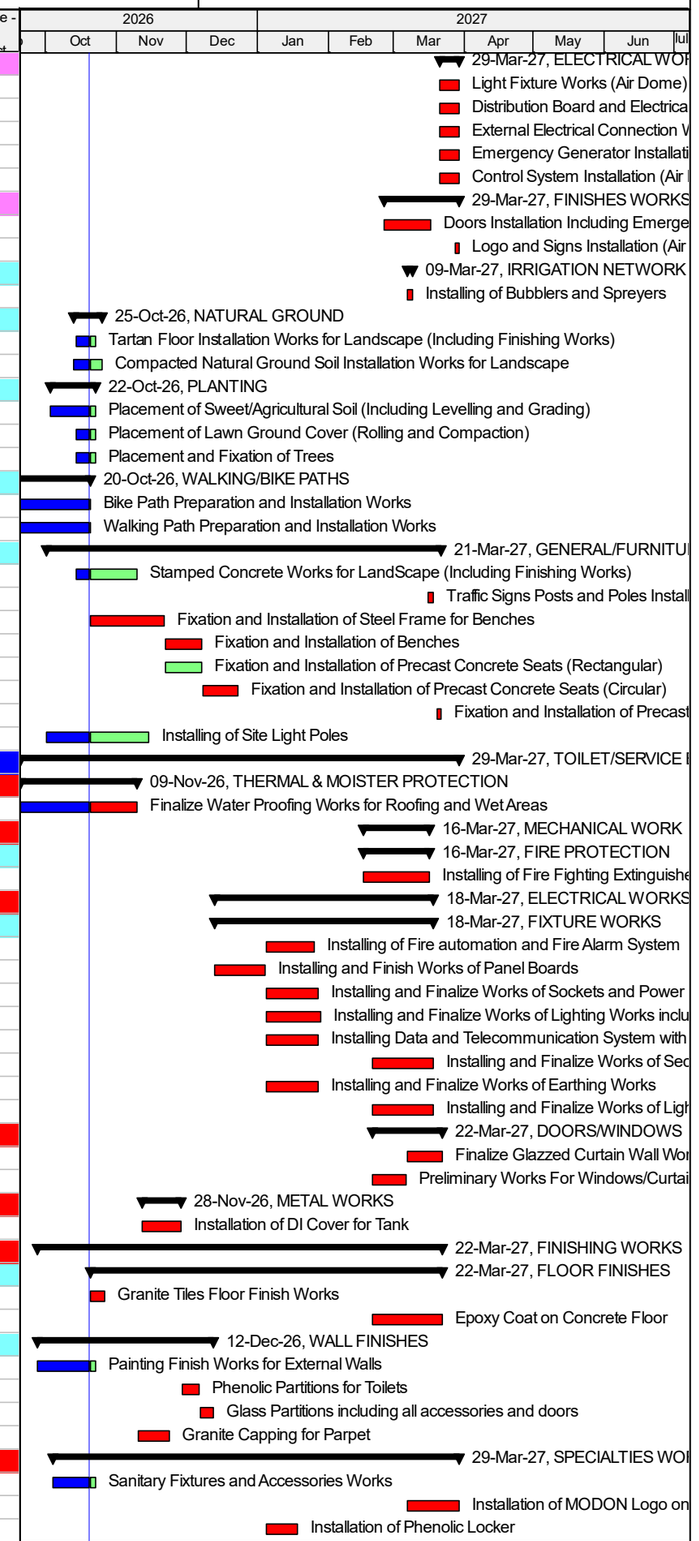

Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary


TASK filter: Remaining works.

© Oracle Corporation

MLTX-02-005 - Playground Initiative for Eastern Region (Arar-Hasa osis -Dammam)

Remaining work
D.D 19-10-2026

Activity ID	Activity Name	Original Duration	Schedule % Complete	Performance % Complete	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Variance - BL Project
TESTING & COMMISSIONING		23	0%	0%	08-Dec-26	02-Jan-27	24-Mar-27	19-Apr-27	0.00	0.00	0.00	-88
MLTX-02-005-TC-11890	Testing and Commissioning for MEP Works for Playground	18	0%	0%	12-Dec-26	31-Dec-26	30-Mar-27	19-Apr-27	0.00	0.00	0.00	-89
MLTX-02-005-TC-11900	Testing and Commissioning for MEP Works for Toilet/Service	7	0%	0%	26-Dec-26	02-Jan-27	10-Apr-27	17-Apr-27	0.00	0.00	0.00	-86
MLTX-02-005-TC-11910	Testing and Commissioning for MEP Works for Landscape	21	0%	0%	08-Dec-26	31-Dec-26	24-Mar-27	17-Apr-27	0.00	0.00	0.00	-87
DAMMAM		175	7.57%	1.69%	16-Apr-26	02-Jan-27	06-Sep-26 A	15-Mar-27	473,298.71	105,878.30	6,251,922.91	-58
ENGINEERING		70	0%	0%	16-Apr-26	02-Aug-26	20-Oct-26	09-Jan-27	0.00	0.00	0.00	-136
SHOP DRAWINGS		70	0%	0%	16-Apr-26	02-Aug-26	20-Oct-26	09-Jan-27	0.00	0.00	0.00	-136
SHOP DRAWINGS SUBMISSION		30	0%	0%	16-Apr-26	01-Jul-26	20-Oct-26	23-Nov-26	0.00	0.00	0.00	-123
SHOP DRAWINGS SUBMITTALS FOR PLAYGROUND WORKS		30	0%	0%	16-Apr-26	01-Jul-26	20-Oct-26	23-Nov-26	0.00	0.00	0.00	-123
AIR DOME SYSTEM		30	0%	0%	16-Apr-26	07-Jun-26	20-Oct-26	23-Nov-26	0.00	0.00	0.00	-144
MLTX-02-005-EI	Shop DWG Submittal for Cable Tension Layout	15	100%	0%	16-Apr-26	03-May-26	20-Oct-26	05-Nov-26	0.00	0.00	0.00	-156
MLTX-02-005-EI	Shop DWG Submittal for Airlock Door Details	25	100%	0%	30-Apr-26	01-Jun-26	20-Oct-26	17-Nov-26	0.00	0.00	0.00	-144
MLTX-02-005-EI	Shop DWG Submittal for Emergency Exit Details	30	100%	0%	30-Apr-26	07-Jun-26	20-Oct-26	23-Nov-26	0.00	0.00	0.00	-144
MECHANCAL WORKS		15	0%	0%	30-Apr-26	14-Jun-26	20-Oct-26	05-Nov-26	0.00	0.00	0.00	-123
MLTX-02-005-EI	Shop DWG Submittal for HVAC Plan	15	100%	0%	30-Apr-26	17-May-26	20-Oct-26	05-Nov-26	0.00	0.00	0.00	-144
MLTX-02-005-EI	Shop DWG Submittal for Exhaust Air Plan	15	100%	0%	25-May-26	14-Jun-26	20-Oct-26	05-Nov-26	0.00	0.00	0.00	-123
ELECTRICAL WORKS		30	0%	0%	25-May-26	01-Jul-26	20-Oct-26	23-Nov-26	0.00	0.00	0.00	-123
MLTX-02-005-EI	Shop DWG Submittal for Power Layout	25	100%	0%	25-May-26	25-Jun-26	20-Oct-26	17-Nov-26	0.00	0.00	0.00	-123
MLTX-02-005-EI	Shop DWG Submittal for Power Single Line Diagram	25	100%	0%	25-May-26	25-Jun-26	20-Oct-26	17-Nov-26	0.00	0.00	0.00	-123
MLTX-02-005-EI	Shop DWG Submittal for Panel Board Schedules	25	100%	0%	25-May-26	25-Jun-26	20-Oct-26	17-Nov-26	0.00	0.00	0.00	-123
MLTX-02-005-EI	Shop DWG Submittal for Power Installation Details	30	100%	0%	25-May-26	01-Jul-26	20-Oct-26	23-Nov-26	0.00	0.00	0.00	-123
SHOP DRAWINGS APPROVALS		70	0%	0%	30-Apr-26	02-Aug-26	20-Oct-26	09-Jan-27	0.00	0.00	0.00	-136
SHOP DRAWINGS APPROVAL FOR PLAYGROUND WORKS		70	0%	0%	30-Apr-26	02-Aug-26	20-Oct-26	09-Jan-27	0.00	0.00	0.00	-136
AIR DOME SYSTEM		60	0%	0%	30-Apr-26	12-Jul-26	20-Oct-26	28-Dec-26	0.00	0.00	0.00	-144
MLTX-02-005-EI	Shop DWG Approval for Air Dome Structural Layout	15	100%	0%	30-Apr-26	17-May-26	20-Oct-26	05-Nov-26	0.00	0.00	0.00	-144
MLTX-02-005-EI	Shop DWG Approval for Membrane Panel Layout	15	100%	0%	18-May-26	07-Jun-26	07-Nov-26	23-Nov-26	0.00	0.00	0.00	-144
MLTX-02-005-EI	Shop DWG Approval for Cable Tension Layout	15	100%	0%	18-May-26	07-Jun-26	07-Nov-26	23-Nov-26	0.00	0.00	0.00	-144
MLTX-02-005-EI	Shop DWG Approval for Airlock Door Details	15	100%	0%	08-Jun-26	24-Jun-26	24-Nov-26	10-Dec-26	0.00	0.00	0.00	-144
MLTX-02-005-EI	Shop DWG Approval for Emergency Exit Details	15	100%	0%	25-Jun-26	12-Jul-26	12-Dec-26	28-Dec-26	0.00	0.00	0.00	-144
SPORTS EQUIPMENT		30	0%	0%	25-May-26	01-Jul-26	20-Oct-26	23-Nov-26	0.00	0.00	0.00	-123
MLTX-02-005-EI	Shop DWG Approval for Football Turf Installation	30	100%	0%	25-May-26	01-Jul-26	20-Oct-26	23-Nov-26	0.00	0.00	0.00	-123
MECHANCAL WORKS		40	0%	0%	18-May-26	06-Jul-26	07-Nov-26	22-Dec-26	0.00	0.00	0.00	-144
MLTX-02-005-EI	Shop DWG Approval for HVAC Plan	25	100%	0%	18-May-26	18-Jun-26	07-Nov-26	05-Dec-26	0.00	0.00	0.00	-144
MLTX-02-005-EI	Shop DWG Approval for Exhaust Air Plan	15	100%	0%	20-Jun-26	06-Jul-26	06-Dec-26	22-Dec-26	0.00	0.00	0.00	-144
ELECTRICAL WORKS		45	0%	0%	27-Jun-26	02-Aug-26	18-Nov-26	09-Jan-27	0.00	0.00	0.00	-136
MLTX-02-005-EI	Shop DWG Approval for Power Layout	25	100%	0%	02-Jul-26	30-Jul-26	24-Nov-26	22-Dec-26	0.00	0.00	0.00	-123
MLTX-02-005-EI	Shop DWG Approval for Power Single Line Diagram	25	100%	0%	27-Jun-26	25-Jul-26	18-Nov-26	16-Dec-26	0.00	0.00	0.00	-123
MLTX-02-005-EI	Shop DWG Approval for Panel Board Schedules	25	100%	0%	27-Jun-26	25-Jul-26	18-Nov-26	16-Dec-26	0.00	0.00	0.00	-123
MLTX-02-005-EI	Shop DWG Approval for Power Installation Details	15	100%	0%	16-Jul-26	02-Aug-26	23-Dec-26	09-Jan-27	0.00	0.00	0.00	-136
PROCUREMENT		97	0%	0%	21-May-26	21-Dec-26	20-Oct-26	09-Feb-27	0.00	0.00	0.00	-43
SHORT LEAD ITEM		97	0%	0%	21-May-26	21-Dec-26	20-Oct-26	09-Feb-27	0.00	0.00	0.00	-43
TOILET/SERVICE WORKS		41	0%	0%	17-Jun-26	28-Nov-26	20-Oct-26	06-Dec-26	0.00	0.00	0.00	-7
LIGHTING FIXTURES		10	0%	0%	22-Jul-26	02-Aug-26	23-Nov-26	03-Dec-26	0.00	0.00	0.00	-105
MLTX-02-005-PR-1	Material Delivery for Lighting Fixtures	10	100%	0%	22-Jul-26	02-Aug-26	23-Nov-26	03-Dec-26	0.00	0.00	0.00	-105
SWITCHES/SOCKETS		12	0%	0%	22-Jul-26	04-Aug-26	23-Nov-26	06-Dec-26	0.00	0.00	0.00	-105
MLTX-02-005-PR-1	PO for Switches/Sockets	5	100%	0%	22-Jul-26	27-Jul-26	23-Nov-26	28-Nov-26	0.00	0.00	0.00	-105
MLTX-02-005-PR-1	Material Delivery for Switches/Sockets	7	100%	0%	28-Jul-26	04-Aug-26	29-Nov-26	06-Dec-26	0.00	0.00	0.00	-105
DISTRIBUTION PANNELS		40	0%	0%	13-Oct-26	28-Nov-26	20-Oct-26	05-Dec-26	0.00	0.00	0.00	-6
MLTX-02-005-PR-1	PO for Distribution Panels	15	40%	0%	13-Oct-26	29-Oct-26	20-Oct-26	05-Nov-26	0.00	0.00	0.00	-6
MLTX-02-005-PR-1	Material Delivery for Distribution Panels	25	0%	0%	31-Oct-26	28-Nov-26	07-Nov-26	05-Dec-26	0.00	0.00	0.00	-6
FURNITURES		29	0%	0%	17-Jun-26	20-Jul-26	20-Oct-26	22-Nov-26	0.00	0.00	0.00	-106
MLTX-02-005-PR-1	PO for Furnitures	9	100%	0%	17-Jun-26	27-Jun-26	20-Oct-26	29-Oct-26	0.00	0.00	0.00	-106
MLTX-02-005-PR-1	Material Delivery for Furnitures	20	100%	0%	28-Jun-26	20-Jul-26	31-Oct-26	22-Nov-26	0.00	0.00	0.00	-106
PLAYGROUND WORKS		97	0%	0%	21-May-26	21-Dec-26	20-Oct-26	09-Feb-27	0.00	0.00	0.00	-43
PVC MEMBRANE		21	0%	0%	21-May-26	17-Jun-26	20-Oct-26	12-Nov-26	0.00	0.00	0.00	-126
MLTX-02-005-PR-1	Material Delivery for PVC Membrane	21	100%	0%	21-May-26	17-Jun-26	20-Oct-26	12-Nov-26	0.00	0.00	0.00	-126
ARTIFICIAL TURF		12	0%	0%	18-Jun-26	01-Jul-26	14-Nov-26	26-Nov-26	0.00	0.00	0.00	-126
MLTX-02-005-PR-1	Material Delivery for Artificial TURF	12	100%	0%	18-Jun-26	01-Jul-26	14-Nov-26	26-Nov-26	0.00	0.00	0.00	-126
RUBBER GRANULES		12	0%	0%	31-May-26	13-Jun-26	20-Oct-26	02-Nov-26	0.00	0.00	0.00	-121
MLTX-02-005-PR-1	Material Delivery for Rubber Granules	12	100%	0%	31-May-26	13-Jun-26	20-Oct-26	02-Nov-26	0.00	0.00	0.00	-121
PADEL GLASS		28	0%	0%	19-Oct-26	19-Nov-26	07-Nov-26	08-Dec-26	0.00	0.00	0.00	-16
MLTX-02-005-PR-1	Material Delivery for Padel Glass	28	3.57%	0%	19-Oct-26	19-Nov-26	07-Nov-26	08-Dec-26	0.00	0.00	0.00	-16
PADEL WIRE MESH/STEEL SETS		15	0%	0%	06-Jun-26	22-Jun-26	20-Oct-26	05-Nov-26	0.00	0.00	0.00	-116
MLTX-02-005-PR-1	Material Delivery for Wire Mesh/Steel Sets	15	100%	0%	06-Jun-26	22-Jun-26	20-Oct-26	05-Nov-26	0.00	0.00	0.00	-116

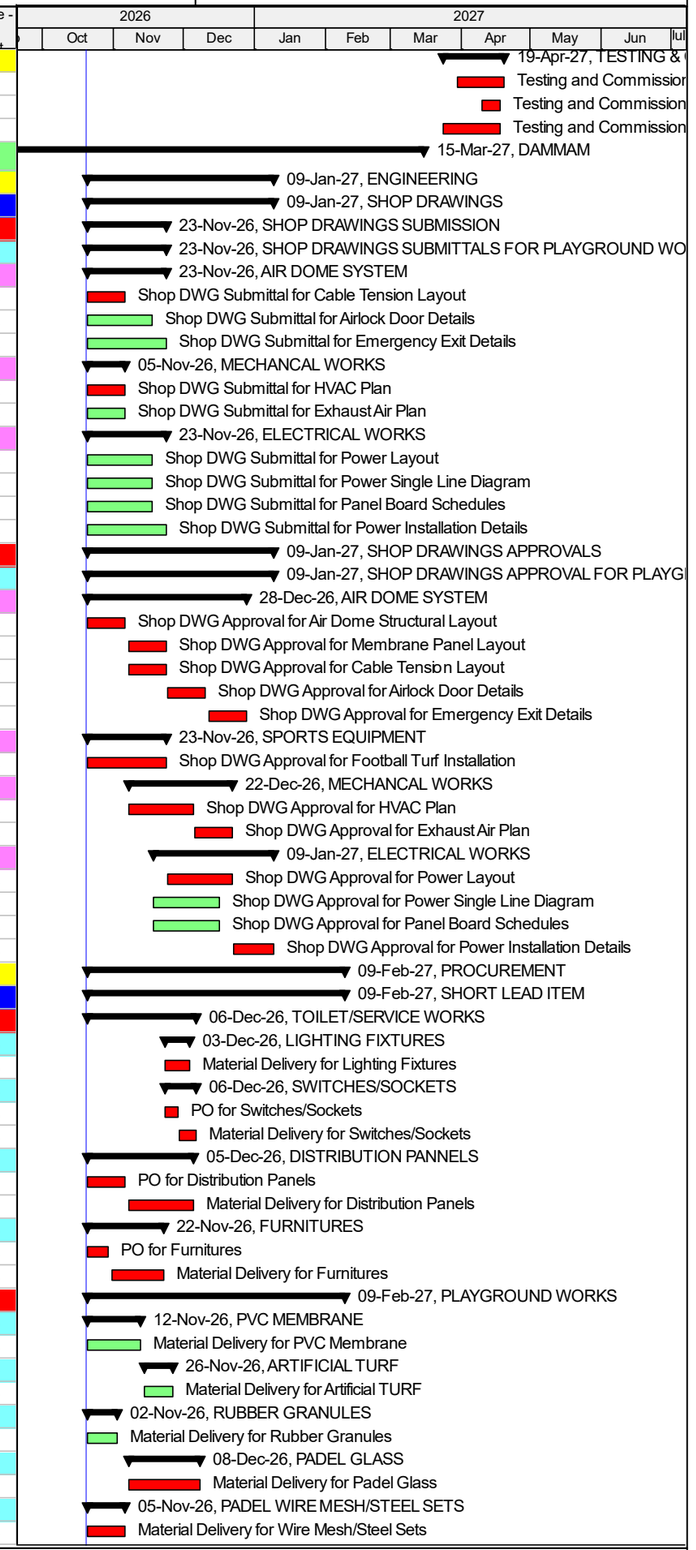

Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary


TASK filter: Remaining works.

© Oracle Corporation

MLTX-02-005 - Playground Initiative for Eastern Region (Arar-Hasa osis -Dammam)

Remaining work
D.D 19-10-2026

Activity ID	Activity Name	Original Duration	Schedule % Complete	Performance % Complete	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Variance - BL Project
BITUMINOUS BASE & WEARING COURSE		32	0%	0%	15-Jun-26	21-Jul-26	10-Nov-26	16-Dec-26	0.00	0.00	0.00	-126
MLTX-02-005-PR-1	PO for Bituminous Base & Wearing Course	15	100%	0%	15-Jun-26	01-Jul-26	10-Nov-26	26-Nov-26	0.00	0.00	0.00	-126
MLTX-02-005-PR-1	Material Delivery for the Site	17	100%	0%	02-Jul-26	21-Jul-26	28-Nov-26	16-Dec-26	0.00	0.00	0.00	-126
INTERLOCKING PAVING		32	0%	0%	09-Aug-26	14-Sep-26	04-Jan-27	09-Feb-27	0.00	0.00	0.00	-126
MLTX-02-005-PR-1	PO for Interlocking Block Pavers	15	100%	0%	09-Aug-26	25-Aug-26	04-Jan-27	20-Jan-27	0.00	0.00	0.00	-126
MLTX-02-005-PR-1	Material Delivery for Interlocking Block Pavers	17	100%	0%	26-Aug-26	14-Sep-26	21-Jan-27	09-Feb-27	0.00	0.00	0.00	-126
MARKING PAINT		32	0%	0%	02-Jul-26	08-Aug-26	28-Nov-26	03-Jan-27	0.00	0.00	0.00	-126
MLTX-02-005-PR-1	PO for Marking Paint	15	100%	0%	02-Jul-26	19-Jul-26	28-Nov-26	14-Dec-26	0.00	0.00	0.00	-126
MLTX-02-005-PR-1	Material Delivery for Marking Paint	17	100%	0%	20-Jul-26	08-Aug-26	15-Dec-26	03-Jan-27	0.00	0.00	0.00	-126
AIR DIFUSSERS/GRILLS		40	0%	0%	01-Oct-26	02-Dec-26	20-Oct-26	05-Dec-26	0.00	0.00	0.00	-2
MLTX-02-005-PR-1	PO for Air Difussers/Grills	15	100%	0%	01-Oct-26	18-Oct-26	20-Oct-26	05-Nov-26	0.00	0.00	0.00	-16
MLTX-02-005-PR-1	Material Delivery for Air Difussers/Grills	25	0%	0%	04-Nov-26	02-Dec-26	07-Nov-26	05-Dec-26	0.00	0.00	0.00	-2
GALVANIZED DUCTS		40	0%	0%	19-Oct-26	03-Dec-26	07-Nov-26	22-Dec-26	0.00	0.00	0.00	-16
MLTX-02-005-PR-1	PO for Galvanized Duct	15	6.67%	0%	19-Oct-26	04-Nov-26	07-Nov-26	23-Nov-26	0.00	0.00	0.00	-16
MLTX-02-005-PR-1	Material Delivery for Galvanized Duct	25	0%	0%	05-Nov-26	03-Dec-26	24-Nov-26	22-Dec-26	0.00	0.00	0.00	-16
EXHAUST FANS		40	0%	0%	17-Jun-26	02-Dec-26	20-Oct-26	05-Dec-26	0.00	0.00	0.00	-2
MLTX-02-005-PR-1	PO for Exhaust Fans	15	100%	0%	17-Jun-26	04-Jul-26	20-Oct-26	05-Nov-26	0.00	0.00	0.00	-106
MLTX-02-005-PR-1	Material Delivery for Exhaust Fans	25	0%	0%	04-Nov-26	02-Dec-26	07-Nov-26	05-Dec-26	0.00	0.00	0.00	-2
DISTRIBUTION BOARDS		20	0%	0%	23-Jun-26	26-Nov-26	07-Nov-26	29-Nov-26	0.00	0.00	0.00	-2
MLTX-02-005-PR-1	PO for Distribution Boards	5	100%	0%	23-Jun-26	28-Jun-26	07-Nov-26	11-Nov-26	0.00	0.00	0.00	-116
MLTX-02-005-PR-1	Material Delivery for Distribution Boards	15	0%	0%	10-Nov-26	26-Nov-26	12-Nov-26	29-Nov-26	0.00	0.00	0.00	-2
POWER CABLES		15	0%	0%	29-Jun-26	15-Jul-26	12-Nov-26	29-Nov-26	0.00	0.00	0.00	-116
MLTX-02-005-PR-1	PO for Power Cables	5	100%	0%	29-Jun-26	04-Jul-26	12-Nov-26	17-Nov-26	0.00	0.00	0.00	-116
MLTX-02-005-PR-1	Material Delivery for Power Cables	10	100%	0%	05-Jul-26	15-Jul-26	18-Nov-26	29-Nov-26	0.00	0.00	0.00	-116
LIGHT FIXTURES		20	0%	0%	10-Nov-26	02-Dec-26	18-Nov-26	10-Dec-26	0.00	0.00	0.00	-7
MLTX-02-005-PR-1	Material Delivery for Light Fixtures	20	0%	0%	10-Nov-26	02-Dec-26	18-Nov-26	10-Dec-26	0.00	0.00	0.00	-7
CCTV MATERIALS		80	0%	0%	30-Jul-26	21-Dec-26	20-Oct-26	20-Jan-27	0.00	0.00	0.00	-26
MLTX-02-005-PR-1	PO for CCTV	5	100%	0%	30-Jul-26	04-Aug-26	20-Oct-26	25-Oct-26	0.00	0.00	0.00	-69
MLTX-02-005-PR-1	Material Delivery for CCTV	15	0%	0%	05-Dec-26	21-Dec-26	04-Jan-27	20-Jan-27	0.00	0.00	0.00	-26
POWER OUTLETS/SWITCHES		31	0%	0%	08-Aug-26	08-Dec-26	07-Dec-26	11-Jan-27	0.00	0.00	0.00	-29
MLTX-02-005-PR-1	PO for Power Outlets/Switches	6	100%	0%	08-Aug-26	13-Aug-26	07-Dec-26	13-Dec-26	0.00	0.00	0.00	-103
MLTX-02-005-PR-1	Material Delivery for Power Outlets/Switches	25	0%	0%	10-Nov-26	08-Dec-26	14-Dec-26	11-Jan-27	0.00	0.00	0.00	-29
LANDSCAPE WORKS		91	0%	0%	05-Aug-26	13-Dec-26	20-Oct-26	02-Feb-27	0.00	0.00	0.00	-44
PAVEMENT MARKING		15	0%	0%	15-Aug-26	31-Aug-26	14-Dec-26	30-Dec-26	0.00	0.00	0.00	-103
MLTX-02-005-PR-1	PO for Pavement Markings	5	100%	0%	15-Aug-26	19-Aug-26	14-Dec-26	19-Dec-26	0.00	0.00	0.00	-103
MLTX-02-005-PR-1	Material Delivery for Pavement Markings	10	100%	0%	20-Aug-26	31-Aug-26	20-Dec-26	30-Dec-26	0.00	0.00	0.00	-103
TRAFFIC SIGNS		39	0%	0%	04-Nov-26	13-Dec-26	20-Dec-26	02-Feb-27	0.00	0.00	0.00	-44
MLTX-02-005-PR-1	PO for Traffic Signs	15	0%	0%	04-Nov-26	21-Nov-26	20-Dec-26	05-Jan-27	0.00	0.00	0.00	-39
MLTX-02-005-PR-1	Material Delivery for Traffic Signs	19	0%	0%	22-Nov-26	13-Dec-26	12-Jan-27	02-Feb-27	0.00	0.00	0.00	-44
IRRIGATION PIPES/SPRINKLERS		23	0%	0%	10-Nov-26	30-Nov-26	20-Dec-26	14-Jan-27	0.00	0.00	0.00	-39
MLTX-02-005-PR-1	PO for Irrigation Pipes/Sprinkles	5	0%	0%	10-Nov-26	15-Nov-26	20-Dec-26	24-Dec-26	0.00	0.00	0.00	-34
MLTX-02-005-PR-1	Material Delivery for Irrigation Pipes/Sprinkles	8	0%	0%	22-Nov-26	30-Nov-26	06-Jan-27	14-Jan-27	0.00	0.00	0.00	-39
AGRICULTURE SOIL		37	0%	0%	05-Aug-26	05-Dec-26	20-Oct-26	01-Dec-26	0.00	0.00	0.00	3
MLTX-02-005-PR-1	PO for Agriculture Soil	15	100%	0%	05-Aug-26	22-Aug-26	20-Oct-26	05-Nov-26	0.00	0.00	0.00	-64
MLTX-02-005-PR-1	Material Delivery for Agriculture Soil	22	0%	0%	10-Nov-26	05-Dec-26	07-Nov-26	01-Dec-26	0.00	0.00	0.00	3
TRACK SURFACE		10	0%	0%	10-Nov-26	21-Nov-26	31-Dec-26	11-Jan-27	0.00	0.00	0.00	-44
MLTX-02-005-PR-1	Material Delivery for Track Surface	10	0%	0%	10-Nov-26	21-Nov-26	31-Dec-26	11-Jan-27	0.00	0.00	0.00	-44
GRASS/TREES		15	0%	0%	22-Nov-26	08-Dec-26	12-Jan-27	28-Jan-27	0.00	0.00	0.00	-44
MLTX-02-005-PR-1	Material Delivery for Grass/Trees	15	0%	0%	22-Nov-26	08-Dec-26	12-Jan-27	28-Jan-27	0.00	0.00	0.00	-44
LONG LEAD ITEM		83	0%	0%	21-May-26	30-Nov-26	20-Oct-26	24-Jan-27	0.00	0.00	0.00	-47
PLAYGROUND WORKS		83	0%	0%	21-May-26	30-Nov-26	20-Oct-26	24-Jan-27	0.00	0.00	0.00	-47
STEEL TENSION CABLES		50	0%	0%	21-May-26	19-Oct-26	20-Oct-26	16-Dec-26	0.00	0.00	0.00	-50
MLTX-02-005-PR-1	PO for Steel Tension Cables	8	100%	0%	21-May-26	02-Jun-26	20-Oct-26	28-Oct-26	0.00	0.00	0.00	-126
MLTX-02-005-PR-1	Material Delivery for Steel Tension Cables	15	100%	0%	07-Sep-26	24-Sep-26	10-Nov-26	26-Nov-26	0.00	0.00	0.00	-54
MLTX-02-005-PR-1	Material Fabrication for Steel Tension Cables	10	100%	0%	03-Jun-26	14-Jun-26	29-Oct-26	09-Nov-26	0.00	0.00	0.00	-126
MLTX-02-005-PR-1	Staging time	7	100%	0%	12-Oct-26	19-Oct-26	09-Dec-26	16-Dec-26	0.00	0.00	0.00	-50
EMERGENCY DOORS		48	0%	0%	15-Jun-26	24-Nov-26	10-Nov-26	04-Jan-27	0.00	0.00	0.00	-35
MLTX-02-005-PR-1	PO for Emergency Doors	10	100%	0%	15-Jun-26	25-Jun-26	10-Nov-26	21-Nov-26	0.00	0.00	0.00	-126
MLTX-02-005-PR-1	Material Delivery for Emergency Doors	15	0%	0%	04-Nov-26	21-Nov-26	15-Dec-26	31-Dec-26	0.00	0.00	0.00	-35
MLTX-02-005-PR-1	Material Fabrication for Emergency Doors	20	100%	0%	27-Jun-26	19-Jul-26	22-Nov-26	14-Dec-26	0.00	0.00	0.00	-126
MLTX-02-005-PR-1	Staging time	3	0%	0%	22-Nov-26	24-Nov-26	02-Jan-27	04-Jan-27	0.00	0.00	0.00	-35
PRESSURE UNITS		40	0%	0%	12-Oct-26	30-Nov-26	09-Dec-26	24-Jan-27	0.00	0.00	0.00	-47
MLTX-02-005-PR-1	PO for Pressure Units	10	70%	0%	12-Oct-26	22-Oct-26	09-Dec-26	20-Dec-26	0.00	0.00	0.00	-50
MLTX-02-005-PR-1	Material Delivery for Pressure Units	10	0%	0%	05-Nov-26	16-Nov-26	02-Jan-27	12-Jan-27	0.00	0.00	0.00	-49

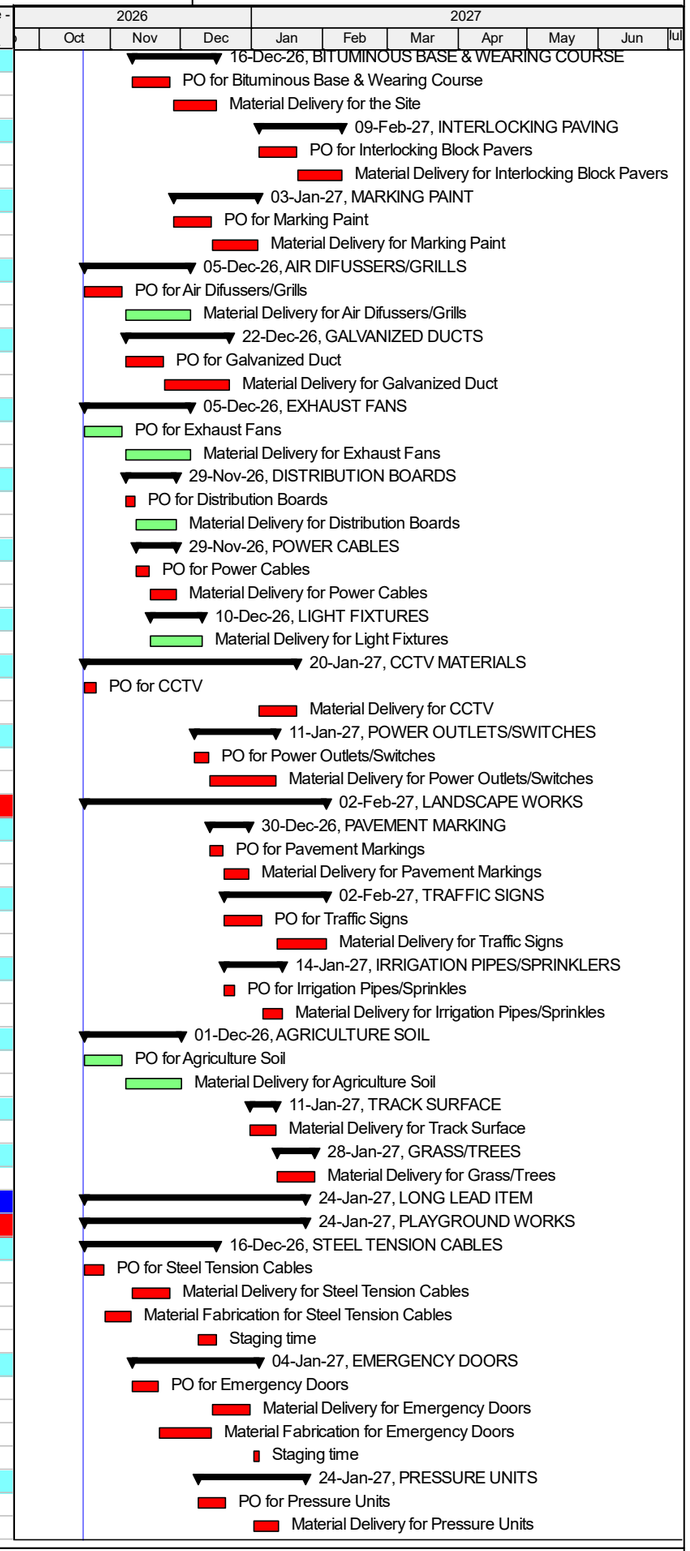

Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary


TASK filter: Remaining works.

© Oracle Corporation

MLTX-02-005 - Playground Initiative for Eastern Region (Arar-Hasa osis -Dammam)

Remaining work
D.D 19-10-2026

Activity ID	Activity Name	Original Duration	Schedule % Complete	Performance % Complete	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Variance - BL Project
MLTX-02-005-PR-1	Material Fabrication for Pressure Units	10	0%	0%	24-Oct-26	03-Nov-26	21-Dec-26	31-Dec-26	0.00	0.00	0.00	-50
MLTX-02-005-PR-1	Staging time	10	0%	0%	19-Nov-26	30-Nov-26	13-Jan-27	24-Jan-27	0.00	0.00	0.00	-47
AIR LOCK DOORS		42	0%	0%	30-Sep-26	26-Nov-26	28-Nov-26	14-Jan-27	0.00	0.00	0.00	-42
MLTX-02-005-PR-1	PO for Lock Doors	10	100%	0%	30-Sep-26	11-Oct-26	28-Nov-26	08-Dec-26	0.00	0.00	0.00	-50
MLTX-02-005-PR-1	Material Delivery for Lock Doors	12	0%	0%	05-Nov-26	18-Nov-26	27-Dec-26	09-Jan-27	0.00	0.00	0.00	-44
MLTX-02-005-PR-1	Material Fabrication for Lock Doors	15	6.67%	0%	19-Oct-26	04-Nov-26	09-Dec-26	26-Dec-26	0.00	0.00	0.00	-44
MLTX-02-005-PR-1	Staging time	5	0%	0%	22-Nov-26	26-Nov-26	10-Jan-27	14-Jan-27	0.00	0.00	0.00	-42
CONSTRUCTION PHASE		175	7.57%	1.69%	02-Jul-26	31-Dec-26	06-Sep-26 A	15-Mar-27	473,298.71	105,878.30	6,251,922.91	-59
SITE WORKS		106	6.57%	1.35%	02-Jul-26	31-Dec-26	15-Oct-26 A	20-Feb-27	385,623.34	79,232.58	5,868,751.92	-43
LANDSCAPE WORKS		106	6.57%	1.35%	02-Jul-26	31-Dec-26	15-Oct-26 A	20-Feb-27	385,623.34	79,232.58	5,868,751.92	-43
PLAYGROUND AREA		70	56.17%	0%	02-Jul-26	31-Dec-26	28-Nov-26	16-Feb-27	338,945.66	0.00	603,475.37	-40
FOOTBALL PLAYGROUND		44	76.92%	0%	02-Jul-26	15-Dec-26	28-Nov-26	17-Jan-27	158,424.99	0.00	205,952.49	-28
MLTX-02-005-CI	Finishing Asphalt & Concrete Surface (Football Playground)	20	100%	0%	02-Jul-26	25-Jul-26	28-Nov-26	20-Dec-26	158,424.99	0.00	158,424.99	-126
MLTX-02-005-CI	Install Sport Equipments - Goal / Nets - (Football Playground)	5	0%	0%	10-Dec-26	15-Dec-26	12-Jan-27	17-Jan-27	0.00	0.00	31,685.00	-28
MLTX-02-005-CI	Surface Marking and Painting (Football Playground)	2	0%	0%	08-Dec-26	09-Dec-26	10-Jan-27	11-Jan-27	0.00	0.00	15,842.50	-28
PADEL PLAYGROUND		5	0%	0%	20-Dec-26	24-Dec-26	06-Feb-27	10-Feb-27	0.00	0.00	70,195.20	-41
MLTX-02-005-CI	Install Sport Equipments - Goal / Nets - (Padel Playground)	5	0%	0%	20-Dec-26	24-Dec-26	06-Feb-27	10-Feb-27	0.00	0.00	58,496.00	-41
MLTX-02-005-CI	Surface Marking and Painting (Padel Playground)	5	0%	0%	20-Dec-26	24-Dec-26	06-Feb-27	10-Feb-27	0.00	0.00	11,699.20	-41
BASKETBALL PLAYGROUND		2	0%	0%	30-Dec-26	31-Dec-26	11-Feb-27	13-Feb-27	0.00	0.00	96,956.10	-37
MLTX-02-005-CI	Install Sport Equipments - Goal / Nets - (Basketball	2	0%	0%	30-Dec-26	31-Dec-26	11-Feb-27	13-Feb-27	0.00	0.00	80,796.75	-37
MLTX-02-005-CI	Surface Marking and Painting (Basketball Playground)	2	0%	0%	30-Dec-26	31-Dec-26	11-Feb-27	13-Feb-27	0.00	0.00	16,159.35	-37
PADEL FENCE		34	0%	0%	26-Nov-26	24-Dec-26	09-Dec-26	17-Jan-27	0.00	0.00	49,850.91	-20
MLTX-02-005-CI	Tempered Glass Fenc Installation and Fixation	25	0%	0%	26-Nov-26	24-Dec-26	09-Dec-26	06-Jan-27	0.00	0.00	30,677.48	-11
MLTX-02-005-CI	Chain Link Fence Installation and Fixation	25	0%	0%	26-Nov-26	24-Dec-26	09-Dec-26	06-Jan-27	0.00	0.00	15,338.75	-11
MLTX-02-005-CI	Install of Fence Gates	5	0%	0%	20-Dec-26	24-Dec-26	12-Jan-27	17-Jan-27	0.00	0.00	3,834.68	-20
CURBSTOEN/INTERLOCK		6	100%	0%	15-Sep-26	21-Sep-26	10-Feb-27	16-Feb-27	180,520.67	0.00	180,520.67	-126
MLTX-02-005-CI	Interlock Installation (Grey Scale) for LandScape (Including	6	100%	0%	15-Sep-26	21-Sep-26	10-Feb-27	16-Feb-27	180,520.67	0.00	180,520.67	-126
AIR DOME		43	0%	0%	15-Nov-26	24-Dec-26	17-Dec-26	04-Feb-27	0.00	0.00	4,306,367.09	-36
CIVIL WORKS		20	0%	0%	15-Nov-26	07-Dec-26	17-Dec-26	09-Jan-27	0.00	0.00	1,391,301.90	-28
MLTX-02-005-CI	Install of Membrane Covering System (Air Dome)	20	0%	0%	15-Nov-26	07-Dec-26	17-Dec-26	09-Jan-27	0.00	0.00	942,830.33	-28
MLTX-02-005-CI	Thermal Insulation Works (Air Dome)	20	0%	0%	15-Nov-26	07-Dec-26	17-Dec-26	09-Jan-27	0.00	0.00	448,471.57	-28
MECHANICAL WORKS		5	0%	0%	08-Dec-26	13-Dec-26	25-Jan-27	30-Jan-27	0.00	0.00	1,233,296.81	-41
MLTX-02-005-CI	Air Ducts and Grills Installation (Air Dome)	4	0%	0%	08-Dec-26	12-Dec-26	25-Jan-27	28-Jan-27	0.00	0.00	728,766.30	-41
MLTX-02-005-CI	Air Units Installation (Air Dome)	5	0%	0%	08-Dec-26	13-Dec-26	25-Jan-27	30-Jan-27	0.00	0.00	336,353.67	-41
MLTX-02-005-CI	Exhaust Fans and Ducts Installation (Air Dome)	5	0%	0%	08-Dec-26	13-Dec-26	25-Jan-27	30-Jan-27	0.00	0.00	168,176.84	-41
ELECTRICAL WORKS		10	0%	0%	08-Dec-26	24-Dec-26	25-Jan-27	04-Feb-27	0.00	0.00	1,513,591.54	-36
MLTX-02-005-CI	Light Fixture Works (Air Dome)	10	0%	0%	08-Dec-26	19-Dec-26	25-Jan-27	04-Feb-27	0.00	0.00	224,235.78	-41
MLTX-02-005-CI	Distribution Board and Electrical Works (Air Dome)	7	0%	0%	12-Dec-26	19-Dec-26	28-Jan-27	04-Feb-27	0.00	0.00	168,176.84	-41
MLTX-02-005-CI	External Electrical Connection Works (Air Dome)	6	0%	0%	13-Dec-26	19-Dec-26	30-Jan-27	04-Feb-27	0.00	0.00	168,176.84	-41
MLTX-02-005-CI	Emergency Generator Installation (Air Dome)	4	0%	0%	15-Dec-26	19-Dec-26	01-Feb-27	04-Feb-27	0.00	0.00	504,530.51	-41
MLTX-02-005-CI	Control System Installation (Air Dome)	3	0%	0%	22-Dec-26	24-Dec-26	02-Feb-27	04-Feb-27	0.00	0.00	448,471.57	-36
FINISHES WORKS		4	0%	0%	12-Dec-26	15-Dec-26	28-Jan-27	01-Feb-27	0.00	0.00	168,176.84	-41
MLTX-02-005-CI	Doors Installation Including Emergency, Entrance doors (Air	2	0%	0%	12-Dec-26	13-Dec-26	28-Jan-27	30-Jan-27	0.00	0.00	112,117.89	-41
MLTX-02-005-CI	Logo and Signs Installation (Air Dome)	2	0%	0%	14-Dec-26	15-Dec-26	31-Jan-27	01-Feb-27	0.00	0.00	56,058.95	-41
IRRIGATION NETWORK		2	0%	0%	01-Dec-26	02-Dec-26	23-Jan-27	24-Jan-27	0.00	0.00	25,106.20	-45
MLTX-02-005-CN-1	Installing of Bubblers and Spreyers	2	0%	0%	01-Dec-26	02-Dec-26	23-Jan-27	24-Jan-27	0.00	0.00	25,106.20	-45
NATURAL GROUND		30	20.34%	0%	10-Oct-26	12-Nov-26	20-Oct-26	23-Nov-26	39,000.00	0.00	191,740.00	-9
MLTX-02-005-CN-1	Tartan Floor Installation Works for Landscape (Including	15	0%	0%	27-Oct-26	12-Nov-26	07-Nov-26	23-Nov-26	0.00	0.00	126,740.00	-9
MLTX-02-005-CN-1	Compacted Natural Ground Soil Installation Works for	15	60%	0%	10-Oct-26	26-Oct-26	20-Oct-26	05-Nov-26	39,000.00	0.00	65,000.00	-9
PLANTING		23	0%	0%	06-Dec-26	31-Dec-26	25-Jan-27	20-Feb-27	0.00	0.00	347,251.46	-43
MLTX-02-005-CN-1	Placement of Sweet/Agricultural Soil (Including Levelling and	6	0%	0%	06-Dec-26	12-Dec-26	25-Jan-27	31-Jan-27	0.00	0.00	104,175.44	-43
MLTX-02-005-CN-1	Placement of Lawn Ground Cover (Rolling and Compaction)	7	0%	0%	24-Dec-26	31-Dec-26	13-Feb-27	20-Feb-27	0.00	0.00	141,732.50	-43
MLTX-02-005-CN-1	Placement and Fixation of Trees	10	0%	0%	13-Dec-26	23-Dec-26	01-Feb-27	11-Feb-27	0.00	0.00	101,343.52	-43
GENERAL/FURNITURE		81	1.94%	20.07%	11-Oct-26	31-Dec-26	15-Oct-26 A	20-Feb-27	7,677.68	79,232.58	394,811.80	-43
MLTX-02-005-CN-1	Stamped Concrete Works for LandScape (Including	18	0%	0%	01-Nov-26	21-Nov-26	09-Dec-26	29-Dec-26	0.00	0.00	93,594.00	-33
MLTX-02-005-CN-1	Traffic Signs Posts and Poles Installation	15	0%	0%	15-Dec-26	31-Dec-26	03-Feb-27	20-Feb-27	0.00	0.00	9,749.30	-43
MLTX-02-005-CN-1	Fixation and Installation of Steel Frame for Benches	18	44.44%	0%	11-Oct-26	31-Oct-26	18-Nov-26	08-Dec-26	7,677.68	0.00	17,274.79	-33
MLTX-02-005-CN-1	Fixation and Installation of Benches	20	0%	0%	01-Nov-26	23-Nov-26	30-Dec-26	21-Jan-27	0.00	0.00	40,307.84	-51
MLTX-02-005-CN-1	Fixation and Installation of Precast Concrete Seats	20	0%	0%	01-Nov-26	23-Nov-26	30-Dec-26	21-Jan-27	0.00	0.00	32,757.76	-51
MLTX-02-005-CN-1	Fixation and Installation of Precast Concrete Seats (Circular)	20	0%	0%	01-Nov-26	23-Nov-26	30-Dec-26	21-Jan-27	0.00	0.00	12,869.04	-51
MLTX-02-005-CN-1	Fixation and Installation of Precast Concrete Trash Bins	18	0%	0%	24-Nov-26	14-Dec-26	23-Jan-27	11-Feb-27	0.00	0.00	12,186.67	-51
MLTX-02-005-CN-1	Installing of Site Light Poles	20	0%	45%	22-Nov-26	14-Dec-26	15-Oct-26 A	11-Nov-26	0.00	79,232.58	176,072.40	28
TOILET/SERVICE BUILDING		175	22.88%	6.95%	18-Aug-26	29-Dec-26	06-Sep-26 A	15-Mar-27	87,675.37	26,645.72	383,170.99	-61
THERMAL & MOISTER PROTECTION		8	100%	90%	18-Aug-26	26-Aug-26	06-Sep-26 A	28-Oct-26	16,607.28	14,946.55	16,607.28	-53

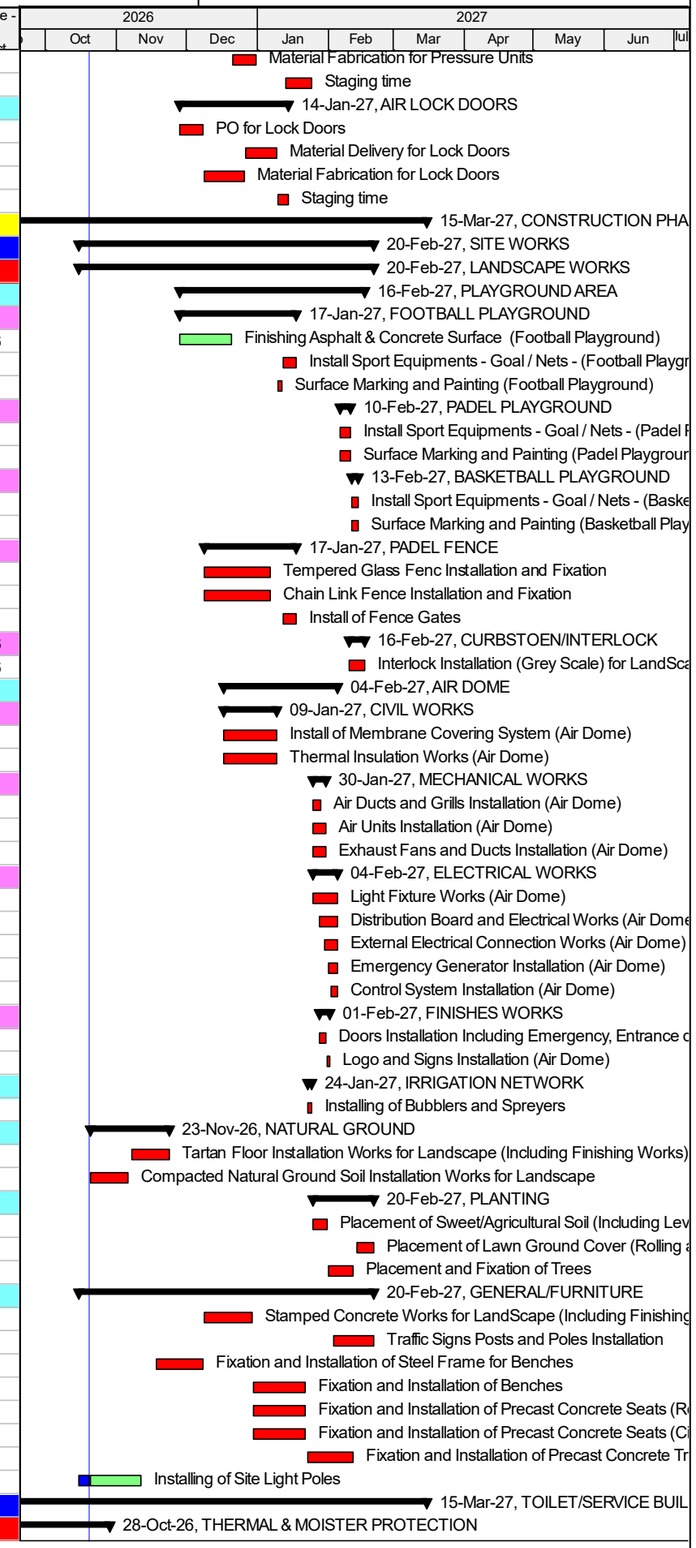

Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary


TASK filter: Remaining works.

© Oracle Corporation

MLTX-02-005 - Playground Initiative for Eastern Region (Arar-Hasa osis -Dammam)

Remaining work
D.D 19-10-2026

Activity ID	Activity Name	Original Duration	Schedule % Complete	Performance % Complete	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Variance - BL Project
MLTX-02-005-CN-140	Finalize Water Proofing Works for Roofing and Wet Areas	8	100%	90%	18-Aug-26	26-Aug-26	06-Sep-26 A	28-Oct-26	16,607.28	14,946.55	16,607.28	-53
MECHANICAL WORK		12	0%	0%	13-Dec-26	26-Dec-26	06-Jan-27	19-Jan-27	0.00	0.00	1,949.87	-21
FIRE PROTECTION		12	0%	0%	13-Dec-26	26-Dec-26	06-Jan-27	19-Jan-27	0.00	0.00	1,949.87	-21
MLTX-02-005-CN-1	Installing of Fire Fighting Extinguisher and accessories	12	0%	0%	13-Dec-26	26-Dec-26	06-Jan-27	19-Jan-27	0.00	0.00	1,949.87	-21
ELECTRICAL WORKS		37	0%	0%	23-Nov-26	29-Dec-26	06-Jan-27	17-Feb-27	0.00	0.00	180,781.27	-43
FIXTURE WORKS		37	0%	0%	23-Nov-26	29-Dec-26	06-Jan-27	17-Feb-27	0.00	0.00	180,781.27	-43
MLTX-02-005-CN-1	Installing of Fire automation and Fire Alarm System	15	0%	0%	12-Dec-26	28-Dec-26	23-Jan-27	08-Feb-27	0.00	0.00	34,317.53	-36
MLTX-02-005-CN-1	Installing and Finish Works of Panel Boards	21	0%	0%	06-Dec-26	29-Dec-26	06-Jan-27	30-Jan-27	0.00	0.00	102,367.69	-27
MLTX-02-005-CN-1	Installing and Finalize Works of Sockets and Power Points	13	0%	0%	12-Dec-26	26-Dec-26	23-Jan-27	06-Feb-27	0.00	0.00	7,085.10	-36
MLTX-02-005-CN-1	Installing and Finalize Works of Lighting Works including Light	14	0%	0%	12-Dec-26	27-Dec-26	23-Jan-27	07-Feb-27	0.00	0.00	14,259.43	-36
MLTX-02-005-CN-1	Installing Data and Telecommunication System with all	14	0%	0%	12-Dec-26	27-Dec-26	23-Jan-27	07-Feb-27	0.00	0.00	6,239.59	-36
MLTX-02-005-CN-1	Installing and Finalize Works of Security and Access Control	14	0%	0%	25-Nov-26	10-Dec-26	06-Jan-27	21-Jan-27	0.00	0.00	7,250.09	-36
MLTX-02-005-CN-1	Installing and Finalize Works of Earthing Works	23	0%	0%	23-Nov-26	19-Dec-26	06-Jan-27	01-Feb-27	0.00	0.00	6,824.51	-38
MLTX-02-005-CN-1	Installing and Finalize Works of Lightning Protection System	15	0%	0%	13-Dec-26	29-Dec-26	01-Feb-27	17-Feb-27	0.00	0.00	2,437.33	-43
DOORS/WINDOWS		95	90%	0%	19-Sep-26	27-Dec-26	20-Oct-26	07-Feb-27	52,646.24	0.00	58,495.82	-36
MLTX-02-005-CN-144	Finalize Glazzed Curtain Wall Works	14	0%	0%	12-Dec-26	27-Dec-26	23-Jan-27	07-Feb-27	0.00	0.00	5,849.58	-36
MLTX-02-005-CN-145	Preliminary Works For Windows/Curtain Wall	12	100%	0%	19-Sep-26	03-Oct-26	20-Oct-26	02-Nov-26	52,646.24	0.00	52,646.24	-26
METAL WORKS		28	82.86%	0%	10-Sep-26	26-Oct-26	12-Nov-26	14-Dec-26	8,077.99	0.00	9,749.30	-42
MLTX-02-005-CN-140	Installation of Galvanized Steel Ladder	14	100%	0%	10-Sep-26	27-Sep-26	12-Nov-26	28-Nov-26	5,849.58	0.00	5,849.58	-53
MLTX-02-005-CN-142	Installation of DI Cover for Tank	14	57.14%	0%	11-Oct-26	26-Oct-26	29-Nov-26	14-Dec-26	2,228.41	0.00	3,899.72	-42
FINISHING WORKS		73	18.12%	0%	27-Aug-26	21-Dec-26	29-Oct-26	21-Jan-27	10,343.86	0.00	57,091.62	-27
FLOOR FINISHES		69	53.57%	0%	17-Oct-26	21-Dec-26	03-Nov-26	21-Jan-27	2,193.61	0.00	4,094.76	-27
MLTX-02-005-CN-1	Granite Tiles Floor Finish Works	4	75%	0%	17-Oct-26	20-Oct-26	03-Nov-26	07-Nov-26	2,193.61	0.00	2,924.82	-15
MLTX-02-005-CN-1	Epoxy Coat on Concrete Floor	14	0%	0%	06-Dec-26	21-Dec-26	06-Jan-27	21-Jan-27	0.00	0.00	1,169.94	-27
WALL FINISHES		59	15.38%	0%	27-Aug-26	22-Nov-26	29-Oct-26	05-Jan-27	8,150.24	0.00	52,996.86	-38
MLTX-02-005-CN-1	Phenolic Partitions for Toilets	11	0%	0%	01-Nov-26	12-Nov-26	15-Dec-26	27-Dec-26	0.00	0.00	31,197.60	-38
MLTX-02-005-CN-1	Glass Partitions including all accessories and doors	6	0%	0%	16-Nov-26	22-Nov-26	30-Dec-26	05-Jan-27	0.00	0.00	13,649.02	-38
MLTX-02-005-CN-1	Granite Capping for Parpet	12	100%	0%	27-Aug-26	09-Sep-26	29-Oct-26	11-Nov-26	8,150.24	0.00	8,150.24	-53
SPECIALTIES WORK		63	0%	20%	27-Oct-26	23-Dec-26	12-Oct-26 A	15-Mar-27	0.00	11,699.17	58,495.83	-66
MLTX-02-005-CN-141	Sanitary Fixtures and Accessories Works	4	0%	80%	27-Oct-26	31-Oct-26	12-Oct-26 A	14-Dec-26	0.00	11,699.17	14,623.96	-38
MLTX-02-005-CN-141	Installation of MODON Logo on the entrance	15	0%	0%	07-Dec-26	23-Dec-26	23-Feb-27	15-Mar-27	0.00	0.00	19,498.61	-66
MLTX-02-005-CN-145	Installation of Phenolic Locker	2	0%	0%	14-Nov-26	15-Nov-26	28-Dec-26	29-Dec-26	0.00	0.00	24,373.26	-38
TESTING & COMMISSIONING		23	0%	0%	24-Dec-26	02-Jan-27	13-Feb-27	15-Mar-27	0.00	0.00	0.00	-58
MLTX-02-005-TC-11920	Testing and Commissioning for MEP Works for Playground	5	0%	0%	27-Dec-26	31-Dec-26	15-Feb-27	20-Feb-27	0.00	0.00	0.00	-43
MLTX-02-005-TC-11930	Testing and Commissioning for MEP Works for Toilet/Service	3	0%	0%	30-Dec-26	02-Jan-27	09-Mar-27	15-Mar-27	0.00	0.00	0.00	-58
MLTX-02-005-TC-11940	Testing and Commissioning for MEP Works for Landscape	7	0%	0%	24-Dec-26	31-Dec-26	13-Feb-27	20-Feb-27	0.00	0.00	0.00	-43
PROJECT CLOSEOUT & DEMOBILIZATION		24	0%	0%	08-Dec-26	02-Jan-27	24-Mar-27	20-Apr-27	0.00	0.00	0.00	-89
As-Built DWGs		20	0%	0%	08-Dec-26	31-Dec-26	24-Mar-27	15-Apr-27	0.00	0.00	0.00	-86
As-Built DWGs Submittals		16	0%	0%	08-Dec-26	27-Dec-26	24-Mar-27	11-Apr-27	0.00	0.00	0.00	-86
MLTX-02-005-CO-1200(	As-Built DWGs Submittal for Playground Area Works	2	0%	0%	12-Dec-26	13-Dec-26	30-Mar-27	31-Mar-27	0.00	0.00	0.00	-89
MLTX-02-005-CO-1201(	As-Built DWGs Submittal for Toilet/Service Building Works	2	0%	0%	26-Dec-26	27-Dec-26	10-Apr-27	11-Apr-27	0.00	0.00	0.00	-86
MLTX-02-005-CO-1202(	As-Built DWGs Submittal for Landscape Works	4	0%	0%	08-Dec-26	12-Dec-26	24-Mar-27	28-Mar-27	0.00	0.00	0.00	-87
As-Built DWGs Approvals		16	0%	0%	15-Dec-26	31-Dec-26	29-Mar-27	15-Apr-27	0.00	0.00	0.00	-86
MLTX-02-005-CO-1204(	As-Built DWGs Approval for Playground Area Works	3	0%	0%	19-Dec-26	21-Dec-26	01-Apr-27	04-Apr-27	0.00	0.00	0.00	-85
MLTX-02-005-CO-1205(	As-Built DWGs Approval for Toilet/Service Building Works	3	0%	0%	29-Dec-26	31-Dec-26	13-Apr-27	15-Apr-27	0.00	0.00	0.00	-86
MLTX-02-005-CO-1206(	As-Built DWGs Approval for Landscape Works	3	0%	0%	15-Dec-26	17-Dec-26	29-Mar-27	31-Mar-27	0.00	0.00	0.00	-85
Demobilization		8	0%	0%	28-Dec-26	02-Jan-27	12-Apr-27	20-Apr-27	0.00	0.00	0.00	-89
MLTX-02-005-CO-12080	Demobilization of Manpower	1	0%	0%	28-Dec-26	28-Dec-26	12-Apr-27	12-Apr-27	0.00	0.00	0.00	-86
MLTX-02-005-CO-12090	Removal of Equipment from Site	1	0%	0%	28-Dec-26	28-Dec-26	12-Apr-27	12-Apr-27	0.00	0.00	0.00	-86
MLTX-02-005-CO-12100	Site Clean Up	1	0%	0%	31-Dec-26	31-Dec-26	13-Apr-27	13-Apr-27	0.00	0.00	0.00	-84
MLTX-02-005-CO-12110	Restoration of Ground Surfaces	1	0%	0%	02-Jan-27	02-Jan-27	20-Apr-27	20-Apr-27	0.00	0.00	0.00	-89

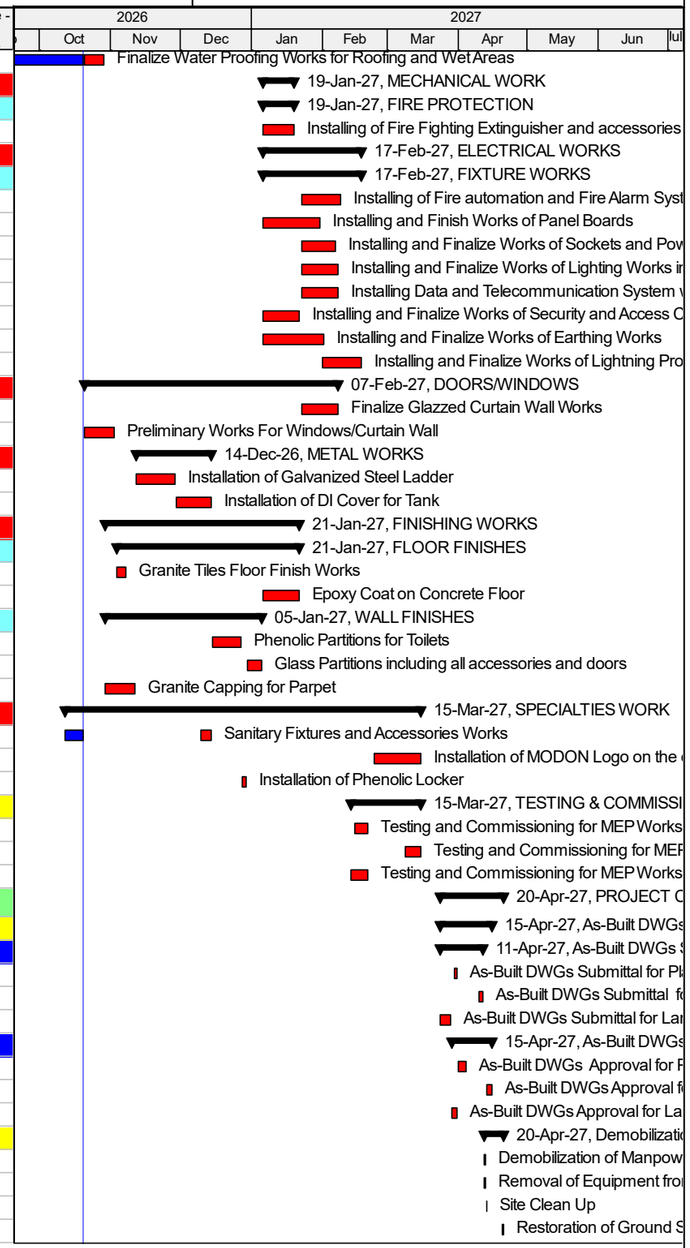

Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary

TASK filter: Remaining works.

© Oracle Corporation
