

Activity ID	Activity Name	Original Duration	BL Project Start	BL Project Finish	Budgeted Total Cost	Planned Value Cost	Earned Value Cost	Schedule % Complete	Performance % Complete
44 READY BUILT FACTORIES 900 m2 IN AL DAMMAM #3		219	12-Feb-26	24-Dec-26	4,736,076.69	2,482,009.60	2,384,162.47	52.41%	50.34%
PROJECT MILESTONES		0	12-Feb-26	12-Feb-26	0.00	0.00	0.00	0%	0%
CONTRACTUAL MILESTONES		0	12-Feb-26	12-Feb-26	0.00	0.00	0.00	0%	0%
DAM3-PMS-MMS-007	Completion of Site levelling, local roads & parkings	0		12-Feb-26	0.00	0.00	0.00	100%	0%
CONSTRUCTION (67%)		219	20-May-26	24-Dec-26	4,672,730.14	2,418,663.04	2,336,652.55	51.76%	50.01%
RBF 900 SQM FACTORIES		219	20-May-26	24-Dec-26	3,515,173.29	1,887,417.66	1,311,551.50	53.69%	37.31%
BLOCK B6		122	20-May-26	07-Nov-26	508,185.53	218,381.17	36,750.08	42.97%	7.23%
STRUCTURAL		1	07-Jun-26	07-Jun-26	16,723.88	16,723.88	16,723.88	100%	100%
COLUMNS & BEAMS		1	07-Jun-26	07-Jun-26	16,723.88	16,723.88	16,723.88	100%	100%
DAM3-C-B6-S-613	Pouring Concrete for Beams	1	07-Jun-26	07-Jun-26	16,723.88	16,723.88	16,723.88	100%	100%
STRUCTURAL STEEL		14	25-May-26	21-Jun-26	142,700.40	142,700.40	0.00	100%	0%
DAM3-C-B6-SS-103	Steel members for office area	7	25-May-26	04-Jun-26	115,805.20	115,805.20	0.00	100%	0%
DAM3-C-B6-SS-104	Epoxy paint to steel members at office area	7	06-Jun-26	13-Jun-26	23,161.04	23,161.04	0.00	100%	0%
DAM3-C-B6-SS-106	Epoxy paint for external platform	5	16-Jun-26	21-Jun-26	3,734.16	3,734.16	0.00	100%	0%
ELECTRICAL		122	20-May-26	07-Nov-26	348,761.25	58,956.90	20,026.20	16.9%	5.74%
FIRST STAGE		122	20-May-26	18-Oct-26	60,725.20	58,956.90	20,026.20	97.09%	32.98%
DAM3-C-B6-E-343	Installation of Earthing and Grounding	4	04-Jul-26	07-Jul-26	19,646.47	19,646.47	17,681.82	100%	90%
DAM3-C-B6-E-413	Installation of Sleeves & Power outlet	8	20-May-26	01-Jun-26	2,920.45	2,920.45	1,460.23	100%	50%
DAM3-C-B6-E-373	Installation of Conduits and wiring outlets - Fire Alarm Syste	4	14-Oct-26	18-Oct-26	1,768.31	0.00	884.15	0%	50%
DAM3-C-B6-E-453	Installation of LV Cables	4	21-Jul-26	25-Jul-26	36,389.98	36,389.98	0.00	100%	0%
SECOND STAGE		8	28-Oct-26	07-Nov-26	288,036.05	0.00	0.00	0%	0%
DAM3-C-B6-E-730	Installation of Solar power plant	7	31-Oct-26	07-Nov-26	253,268.71	0.00	0.00	0%	0%
DAM3-C-B6-E-503	Installation of Access Control System	4	28-Oct-26	01-Nov-26	27,616.86	0.00	0.00	0%	0%
DAM3-C-B6-E-513	Monitor Modules for Fire Alarm	2	02-Nov-26	03-Nov-26	3,882.38	0.00	0.00	0%	0%
DAM3-C-B6-E-523	Line Isolator Modules for Fire Alarm	2	04-Nov-26	05-Nov-26	185.40	0.00	0.00	0%	0%
DAM3-C-B6-E-533	Firewarning flash light with sounder; wall mounted, Weathe	2	04-Nov-26	05-Nov-26	3,082.69	0.00	0.00	0%	0%
BLOCK B5		118	14-Jun-26	23-Nov-26	957,041.11	684,125.93	350,104.01	71.48%	36.58%
STRUCTURAL		7	22-Jun-26	29-Jun-26	907.11	907.11	0.00	100%	0%
SLAB ON GRADE		7	22-Jun-26	29-Jun-26	907.11	907.11	0.00	100%	0%
DAM3-C-B5-S-127	Concrete pad	7	22-Jun-26	29-Jun-26	907.11	907.11	0.00	100%	0%
STRUCTURAL STEEL		9	14-Jun-26	27-Jun-26	353,156.52	353,156.52	293,635.19	100%	83.15%
DAM3-C-B5-SS-300	Installation of wall sandwich panel	5	22-Jun-26	27-Jun-26	326,261.32	326,261.32	293,635.19	100%	90%
DAM3-C-B5-SS-102	Epoxy paint to steel members at office area	7	14-Jun-26	21-Jun-26	23,161.04	23,161.04	0.00	100%	0%
DAM3-C-B5-SS-104	Epoxy paint for external platform	5	22-Jun-26	27-Jun-26	3,734.16	3,734.16	0.00	100%	0%
ARCHITECTURAL		19	28-Jun-26	08-Aug-26	325,373.54	325,373.54	36,442.62	100%	11.2%
WALL FINISHES		15	09-Jul-26	26-Jul-26	48,590.16	48,590.16	36,442.62	100%	75%
DAM3-C-B5-A-145	Internal Wall Plaster	15	09-Jul-26	26-Jul-26	48,590.16	48,590.16	36,442.62	100%	75%
FLOOR FINISHES		7	01-Aug-26	08-Aug-26	46,530.71	46,530.71	0.00	100%	0%
DAM3-C-B5-A-149	Tiles for Toilet	7	01-Aug-26	08-Aug-26	46,530.71	46,530.71	0.00	100%	0%
DOORS & WINDOWS		12	28-Jun-26	11-Jul-26	225,373.65	225,373.65	0.00	100%	0%
DAM3-C-B5-A-183	Window (CW1)	7	28-Jun-26	05-Jul-26	94,173.21	94,173.21	0.00	100%	0%
DAM3-C-B5-A-146	Roll up Shutter Door	1	06-Jul-26	06-Jul-26	68,619.20	68,619.20	0.00	100%	0%
DAM3-C-B5-A-147	Supply and install (D5) 1000*2200mm single leaf steel doc	1	07-Jul-26	07-Jul-26	16,016.16	16,016.16	0.00	100%	0%
DAM3-C-B5-A-153	Supply and install (D4) 800*2200 mm single leaf aluminum	1	08-Jul-26	08-Jul-26	22,737.85	22,737.85	0.00	100%	0%
DAM3-C-B5-A-154	Supply and install (D7) 1000*2200 mm single leaf aluminur	1	09-Jul-26	09-Jul-26	7,811.07	7,811.07	0.00	100%	0%
DAM3-C-B5-A-176	Supply and install (D3) 1000*2200 mm single leaf aluminur	1	11-Jul-26	11-Jul-26	16,016.16	16,016.16	0.00	100%	0%
WATER PROOFING WORKS		4	27-Jul-26	30-Jul-26	4,879.02	4,879.02	0.00	100%	0%
DAM3-C-B5-A-163	Waterproofing membrane for toilets	4	27-Jul-26	30-Jul-26	4,879.02	4,879.02	0.00	100%	0%

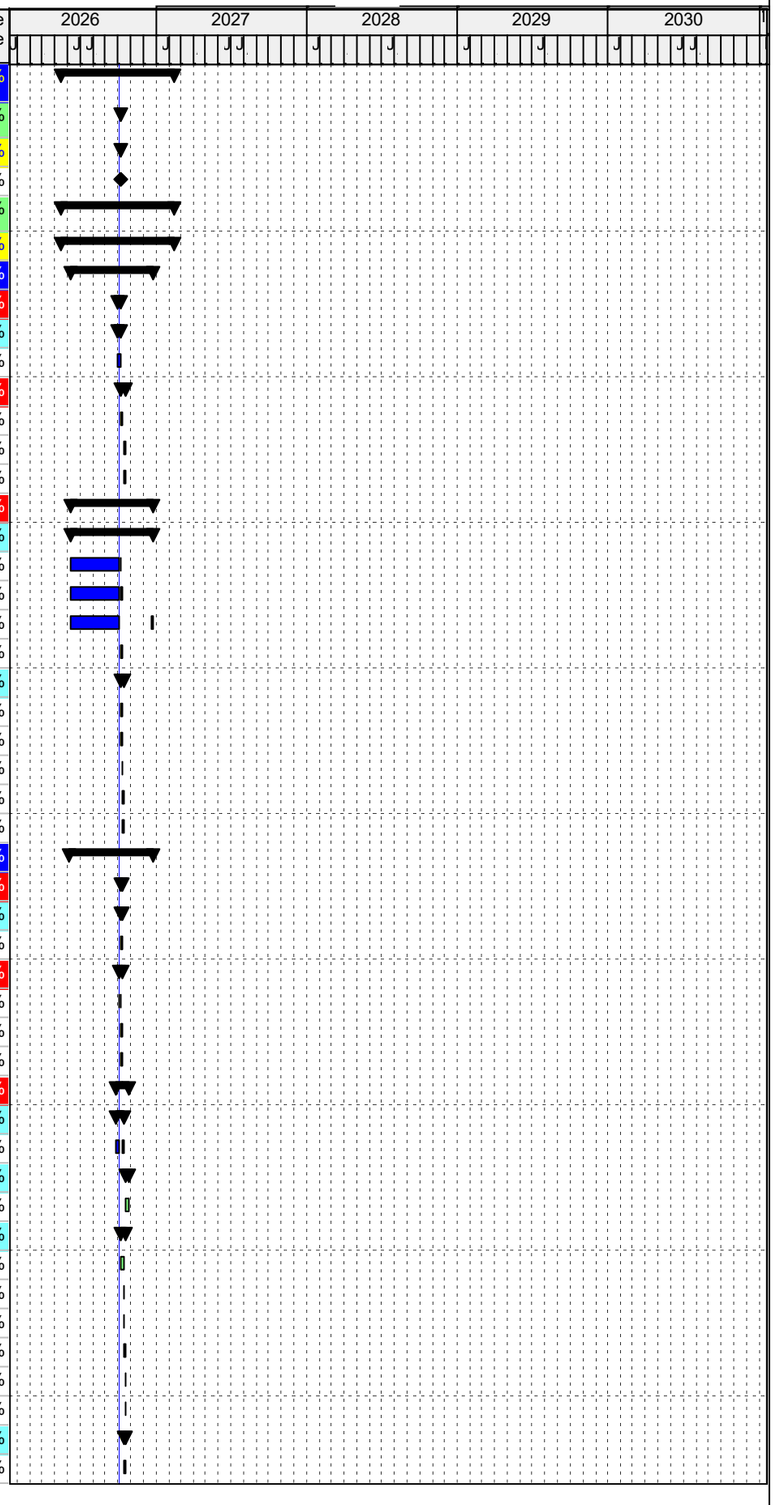

Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary

Date	Revision	Checked	Approved
06-Oct-25	2 Weeks look ahead		


Activity ID	Activity Name	Original Duration	BL Project Start	BL Project Finish	Budgeted Total Cost	Planned Value Cost	Earned Value Cost	Schedule % Complete	Performance % Complete
ELECTRICAL		118	30-Jun-26	23-Nov-26	277,603.94	4,688.76	20,026.20	1.69%	7.21%
FIRST STAGE		118	30-Jun-26	13-Oct-26	24,335.23	4,688.76	20,026.20	19.27%	82.29%
DAM3-C-B5-E-803	Installation of Earthing and Grounding	4	10-Oct-26	13-Oct-26	19,646.47	0.00	17,681.82	0%	90%
DAM3-C-B5-E-833	Installation of Conduits and wiring outlets - Fire Alarm Syste	4	01-Sep-26	05-Sep-26	1,768.31	1,768.31	884.15	100%	50%
DAM3-C-B5-E-873	Installation of Sleeves & Power outlet	8	30-Jun-26	08-Jul-26	2,920.45	2,920.45	1,460.23	100%	50%
SECOND STAGE		14	08-Nov-26	23-Nov-26	253,268.71	0.00	0.00	0%	0%
DAM3-C-B5-E-135	Installation of Solar power plant	14	08-Nov-26	23-Nov-26	253,268.71	0.00	0.00	0%	0%
BLOCK B4		94	28-Jun-26	28-Oct-26	385,954.72	357,845.28	353,904.20	92.72%	91.7%
STRUCTURAL STEEL		22	28-Jun-26	19-Jul-26	353,156.52	353,156.52	326,261.32	100%	92.38%
DAM3-C-B4-A-240	Installation of wall sandwich panel	5	14-Jul-26	19-Jul-26	326,261.32	326,261.32	326,261.32	100%	100%
DAM3-C-B4-SS-10	Epoxy paint for external platform	5	01-Jul-26	06-Jul-26	3,734.16	3,734.16	0.00	100%	0%
DAM3-C-B4-SS-10	Epoxy paint to steel members at office area	7	28-Jun-26	05-Jul-26	23,161.04	23,161.04	0.00	100%	0%
ELECTRICAL		94	22-Jul-26	28-Oct-26	32,798.20	4,688.76	27,642.87	14.3%	84.28%
FIRST STAGE		94	22-Jul-26	28-Oct-26	32,798.20	4,688.76	27,642.87	14.3%	84.28%
DAM3-C-B4-E-573	Installation of Earthing and Grounding	4	25-Oct-26	28-Oct-26	19,646.47	0.00	17,681.82	0%	90%
DAM3-C-B4-E-603	Installation of Conduits and wiring outlets - Fire Alarm Syste	4	24-Sep-26	28-Sep-26	1,768.31	1,768.31	884.15	100%	50%
DAM3-C-B4-E-643	Installation of Sleeves & Power outlet	8	22-Jul-26	30-Jul-26	2,920.45	2,920.45	1,460.23	100%	50%
DAM3-C-B4-E-623	Installation of Conduites for Lighting Fixture	4	08-Oct-26	12-Oct-26	8,462.97	0.00	7,616.67	0%	90%
BLOCK B3		166	20-Jun-26	24-Dec-26	525,864.56	504,449.79	28,388.14	95.93%	5.4%
STRUCTURAL		19	20-Jun-26	18-Jul-26	17,630.99	17,630.99	8,361.94	100%	47.43%
SLAB ON GRADE		7	11-Jul-26	18-Jul-26	907.11	907.11	0.00	100%	0%
DAM3-C-B3-S-101	Concrete pad	7	11-Jul-26	18-Jul-26	907.11	907.11	0.00	100%	0%
COLUMNS & BEAMS		1	20-Jun-26	20-Jun-26	16,723.88	16,723.88	8,361.94	100%	50%
DAM3-C-B3-S-613	Pouring Concrete for Beams	1	20-Jun-26	20-Jun-26	16,723.88	16,723.88	8,361.94	100%	50%
STRUCTURAL STEEL		14	24-Jun-26	15-Jul-26	483,898.34	483,898.34	0.00	100%	0%
DAM3-C-B3-A-1440	Steel members for office area	7	24-Jun-26	01-Jul-26	115,805.20	115,805.20	0.00	100%	0%
DAM3-C-B3-A-240	Installation of wall sandwich panel	5	11-Jul-26	15-Jul-26	326,261.32	326,261.32	0.00	100%	0%
DAM3-C-B3-SS-10	Epoxy paint to steel members at office area	7	02-Jul-26	09-Jul-26	23,161.04	23,161.04	0.00	100%	0%
DAM3-C-B3-SS-10	Steel members for external platform	7	02-Jul-26	09-Jul-26	18,670.78	18,670.78	0.00	100%	0%
ELECTRICAL		166	19-Jul-26	24-Dec-26	24,335.23	2,920.45	20,026.20	12%	82.29%
FIRST STAGE		166	19-Jul-26	24-Dec-26	24,335.23	2,920.45	20,026.20	12%	82.29%
DAM3-C-B3-E-573	Installation of Earthing and Grounding	4	21-Dec-26	24-Dec-26	19,646.47	0.00	17,681.82	0%	90%
DAM3-C-B3-E-643	Installation of Sleeves & Power outlet	5	19-Jul-26	27-Jul-26	2,920.45	2,920.45	1,460.23	100%	50%
DAM3-C-B3-E-603	Installation of Conduits and wiring outlets - Fire Alarm Syste	4	28-Nov-26	01-Dec-26	1,768.31	0.00	884.15	0%	50%
BLOCK B2		37	29-Sep-26	11-Nov-26	24,335.23	3,684.86	20,026.20	15.14%	82.29%
ELECTRICAL		37	29-Sep-26	11-Nov-26	24,335.23	3,684.86	20,026.20	15.14%	82.29%
FIRST STAGE		37	29-Sep-26	11-Nov-26	24,335.23	3,684.86	20,026.20	15.14%	82.29%
DAM3-C-B2-E-143	Installation of Conduits and wiring outlets - Fire Alarm Syste	4	29-Sep-26	04-Oct-26	1,768.31	1,768.31	884.15	100%	50%
DAM3-C-B2-E-113	Installation of Earthing and Grounding	5	05-Nov-26	11-Nov-26	19,646.47	0.00	17,681.82	0%	90%
DAM3-C-B2-E-183	Installation of Sleeves & Power outlet	8	29-Sep-26	08-Oct-26	2,920.45	1,916.55	1,460.23	65.63%	50%
BLOCK B1		65	15-Jul-26	22-Nov-26	44,403.88	20,068.66	20,026.20	45.2%	45.1%
STRUCTURAL		3	15-Jul-26	18-Jul-26	20,068.66	20,068.66	0.00	100%	0%
COLUMNS & BEAMS		3	15-Jul-26	18-Jul-26	20,068.66	20,068.66	0.00	100%	0%
DAM3-C-B1-S-612	Formwork for Beams	2	15-Jul-26	16-Jul-26	3,344.77	3,344.77	0.00	100%	0%
DAM3-C-B1-S-613	Pouring Concrete for Beams	1	18-Jul-26	18-Jul-26	16,723.88	16,723.88	0.00	100%	0%
ELECTRICAL		37	08-Oct-26	22-Nov-26	24,335.23	0.00	20,026.20	0%	82.29%
FIRST STAGE		37	08-Oct-26	22-Nov-26	24,335.23	0.00	20,026.20	0%	82.29%
DAM3-C-B1-E-113	Installation of Earthing and Grounding	5	16-Nov-26	22-Nov-26	19,646.47	0.00	17,681.82	0%	90%
DAM3-C-B1-E-183	Installation of Sleeves & Power outlet	8	08-Oct-26	17-Oct-26	2,920.45	0.00	1,460.23	0%	50%

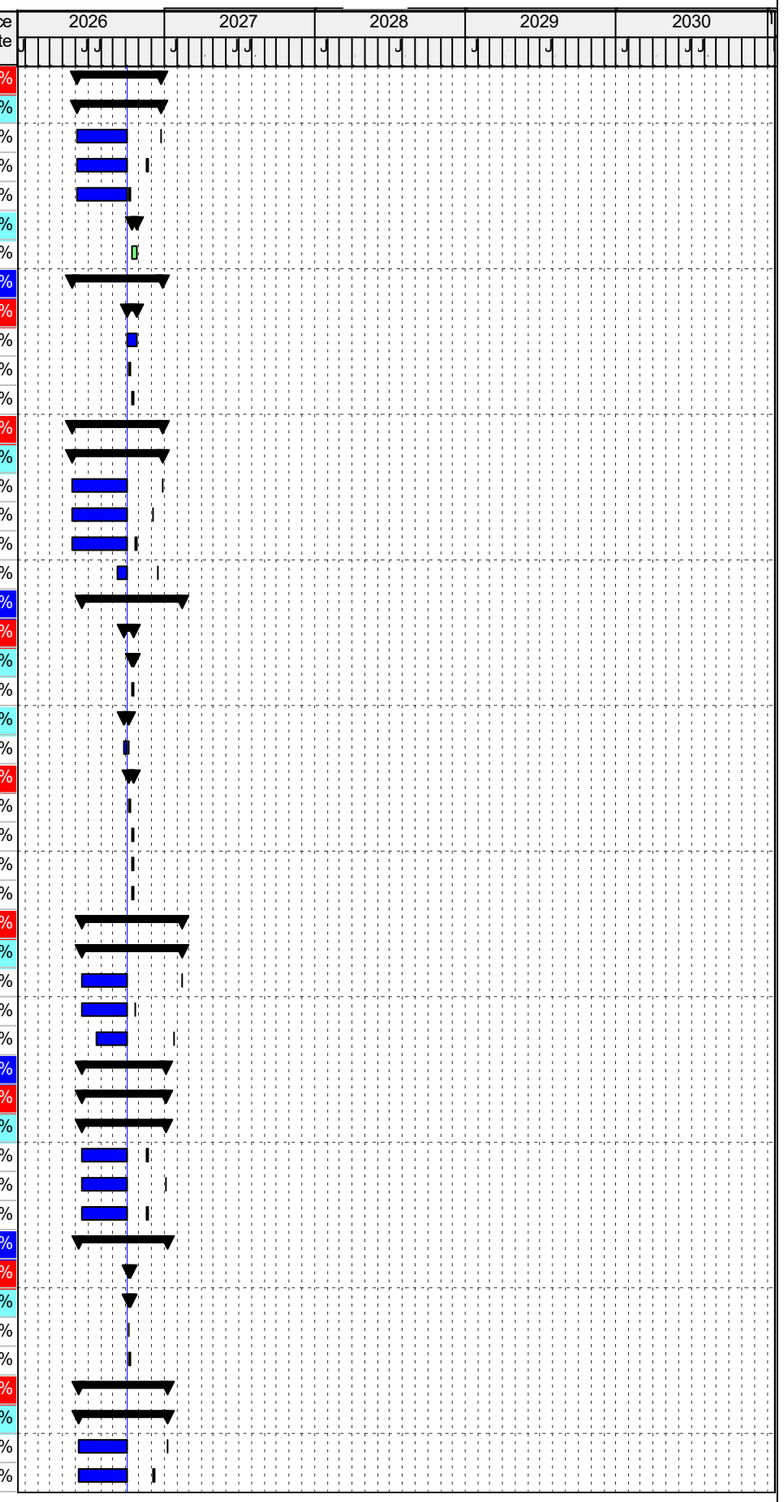

Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary

Date	Revision	Checked	Approved
06-Oct-25	2 Weeks look ahead		


Activity ID	Activity Name	Original Duration	BL Project Start	BL Project Finish	Budgeted Total Cost	Planned Value Cost	Earned Value Cost	Schedule % Complete	Performance % Complete
DAM3-C-B1-E-143	Installation of Conduits and wiring outlets - Fire Alarm Syste	4	08-Oct-26	12-Oct-26	1,768.31	0.00	884.15	0%	50%
BLOCK B7		63	24-Sep-26	30-Nov-26	572,683.54	98,861.97	234,672.97	17.26%	40.98%
ARCHITECTURAL		24	24-Sep-26	28-Nov-26	314,229.27	94,173.21	109,435.41	29.97%	34.83%
WALL FINISHES		4	14-Nov-26	21-Nov-26	44,167.30	0.00	33,125.48	0%	75%
DAM3-C-B7-A-230	Paint to Plaster (Primer, Putty & First Coat)	4	14-Nov-26	21-Nov-26	44,167.30	0.00	33,125.48	0%	75%
DOORS & WINDOWS		7	24-Sep-26	01-Oct-26	94,173.21	94,173.21	23,543.30	100%	25%
DAM3-C-B7-A-552	Window (CW1)	7	24-Sep-26	01-Oct-26	94,173.21	94,173.21	23,543.30	100%	25%
METAL WORKS		5	23-Nov-26	28-Nov-26	175,888.76	0.00	52,766.63	0%	30%
DAM3-C-B7-A-292	Aluminium composite panel	5	23-Nov-26	28-Nov-26	175,888.76	0.00	52,766.63	0%	30%
MECHANICAL		2	29-Nov-26	30-Nov-26	149,489.33	0.00	74,744.66	0%	50%
HVAC		2	29-Nov-26	30-Nov-26	149,489.33	0.00	74,744.66	0%	50%
FIRST STAGE		2	29-Nov-26	30-Nov-26	149,489.33	0.00	74,744.66	0%	50%
DAM3-C-B7-M-14	Installation of HVAC Ducts	2	29-Nov-26	30-Nov-26	149,489.33	0.00	74,744.66	0%	50%
ELECTRICAL		63	27-Sep-26	08-Nov-26	108,964.94	4,688.76	50,492.90	4.3%	46.34%
FIRST STAGE		63	27-Sep-26	08-Nov-26	32,798.20	4,688.76	27,642.87	14.3%	84.28%
DAM3-C-B7-E-113	Installation of Earthing and Grounding	5	03-Nov-26	08-Nov-26	19,646.47	0.00	17,681.82	0%	90%
DAM3-C-B7-E-143	Installation of Conduits and wiring outlets - Fire Alarm Syste	4	27-Sep-26	30-Sep-26	1,768.31	1,768.31	884.15	100%	50%
DAM3-C-B7-E-183	Installation of Sleeves & Power outlet	8	27-Sep-26	05-Oct-26	2,920.45	2,920.45	1,460.23	100%	50%
DAM3-C-B7-E-163	Installation of Conduites for Lighting Fixture	4	11-Oct-26	14-Oct-26	8,462.97	0.00	7,616.67	0%	90%
SECOND STAGE		4	20-Oct-26	24-Oct-26	76,166.74	0.00	22,850.02	0%	30%
DAM3-C-B7-E-153	Installation of Lighting fixtures	4	20-Oct-26	24-Oct-26	76,166.74	0.00	22,850.02	0%	30%
BLOCK B8		61	18-Oct-26	12-Dec-26	76,965.50	0.00	49,726.53	0%	64.61%
ARCHITECTURAL		4	05-Dec-26	12-Dec-26	44,167.30	0.00	22,083.65	0%	50%
WALL FINISHES		4	05-Dec-26	12-Dec-26	44,167.30	0.00	22,083.65	0%	50%
DAM3-C-B8-A-230	Paint to Plaster (Primer, Putty & First Coat)	4	05-Dec-26	12-Dec-26	44,167.30	0.00	22,083.65	0%	50%
ELECTRICAL		61	18-Oct-26	29-Nov-26	32,798.20	0.00	27,642.87	0%	84.28%
FIRST STAGE		61	18-Oct-26	29-Nov-26	32,798.20	0.00	27,642.87	0%	84.28%
DAM3-C-B8-E-113	Installation of Earthing and Grounding	3	24-Nov-26	29-Nov-26	19,646.47	0.00	17,681.82	0%	90%
DAM3-C-B8-E-143	Installation of Conduits and wiring outlets - Fire Alarm Syste	4	18-Oct-26	21-Oct-26	1,768.31	0.00	884.15	0%	50%
DAM3-C-B8-E-183	Installation of Sleeves & Power outlet	8	18-Oct-26	26-Oct-26	2,920.45	0.00	1,460.23	0%	50%
DAM3-C-B8-E-163	Installation of Conduites for Lighting Fixture	4	01-Nov-26	04-Nov-26	8,462.97	0.00	7,616.67	0%	90%
BLOCK B9		77	21-Oct-26	22-Dec-26	255,217.66	0.00	115,307.53	0%	45.18%
ARCHITECTURAL		17	22-Nov-26	22-Dec-26	222,419.46	0.00	87,664.66	0%	39.41%
FLOOR FINISHES		4	22-Nov-26	29-Nov-26	46,530.71	0.00	34,898.03	0%	75%
DAM3-C-B9-A-220	Tiles for Toilet	4	22-Nov-26	29-Nov-26	46,530.71	0.00	34,898.03	0%	75%
METAL WORKS		3	17-Dec-26	22-Dec-26	175,888.76	0.00	52,766.63	0%	30%
DAM3-C-B9-A-292	Aluminium composite panel	3	17-Dec-26	22-Dec-26	175,888.76	0.00	52,766.63	0%	30%
ELECTRICAL		77	21-Oct-26	02-Dec-26	32,798.20	0.00	27,642.87	0%	84.28%
FIRST STAGE		77	21-Oct-26	02-Dec-26	32,798.20	0.00	27,642.87	0%	84.28%
DAM3-C-B9-E-113	Installation of Earthing and Grounding	3	28-Nov-26	02-Dec-26	19,646.47	0.00	17,681.82	0%	90%
DAM3-C-B9-E-143	Installation of Conduits and wiring outlets - Fire Alarm Syste	4	21-Oct-26	25-Oct-26	1,768.31	0.00	884.15	0%	50%
DAM3-C-B9-E-183	Installation of Sleeves & Power outlet	8	21-Oct-26	29-Oct-26	2,920.45	0.00	1,460.23	0%	50%
DAM3-C-B9-E-163	Installation of Conduites for Lighting Fixture	4	04-Nov-26	08-Nov-26	8,462.97	0.00	7,616.67	0%	90%
BLOCK B10		95	08-Oct-26	06-Dec-26	91,596.17	0.00	70,471.91	0%	76.94%
STRUCTURAL STEEL		7	08-Oct-26	15-Oct-26	18,670.78	0.00	14,003.08	0%	75%
DAM3-C-B10-SS-1(	Steel members for external platform	7	08-Oct-26	15-Oct-26	18,670.78	0.00	14,003.08	0%	75%
ARCHITECTURAL		5	03-Nov-26	19-Nov-26	48,590.16	0.00	36,442.62	0%	75%
WALL FINISHES		5	03-Nov-26	19-Nov-26	48,590.16	0.00	36,442.62	0%	75%
DAM3-C-B10-A-18	Internal Wall Plaster	5	03-Nov-26	19-Nov-26	48,590.16	0.00	36,442.62	0%	75%

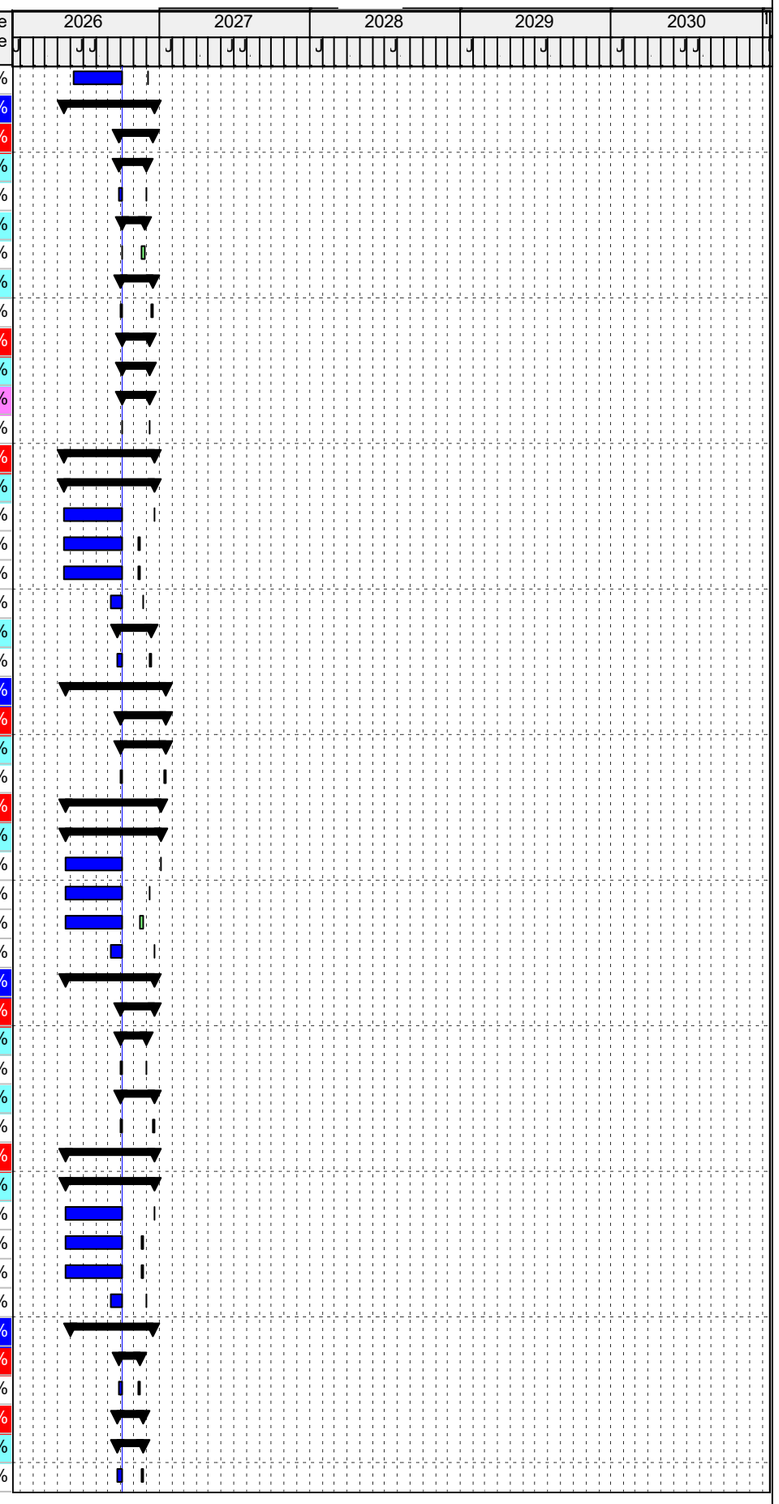

Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary

Date	Revision	Checked	Approved
06-Oct-25	2 Weeks look ahead		

Activity ID	Activity Name	Original Duration	BL Project Start	BL Project Finish	Budgeted Total Cost	Planned Value Cost	Earned Value Cost	Schedule % Complete	Performance % Complete
ELECTRICAL		34	25-Oct-26	06-Dec-26	24,335.23	0.00	20,026.20	0%	82.29%
FIRST STAGE		34	25-Oct-26	06-Dec-26	24,335.23	0.00	20,026.20	0%	82.29%
DAM3-C-B10-E-11	Installation of Earthing and Grounding	5	01-Dec-26	06-Dec-26	19,646.47	0.00	17,681.82	0%	90%
DAM3-C-B10-E-14	Installation of Conduits and wiring outlets - Fire Alarm Syste	4	25-Oct-26	28-Oct-26	1,768.31	0.00	884.15	0%	50%
DAM3-C-B10-E-18	Installation of Sleeves & Power outlet	4	25-Oct-26	02-Nov-26	2,920.45	0.00	1,460.23	0%	50%
BLOCK B11		81	28-Oct-26	09-Dec-26	72,925.39	0.00	32,173.74	0%	44.12%
ARCHITECTURAL		10	07-Nov-26	23-Nov-26	48,590.16	0.00	12,147.54	0%	25%
WALL FINISHES		10	07-Nov-26	23-Nov-26	48,590.16	0.00	12,147.54	0%	25%
DAM3-C-B11-A-18	Internal Wall Plaster	10	07-Nov-26	23-Nov-26	48,590.16	0.00	12,147.54	0%	25%
ELECTRICAL		29	28-Oct-26	09-Dec-26	24,335.23	0.00	20,026.20	0%	82.29%
FIRST STAGE		29	28-Oct-26	09-Dec-26	24,335.23	0.00	20,026.20	0%	82.29%
DAM3-C-B11-E-11	Installation of Earthing and Grounding	3	05-Dec-26	09-Dec-26	19,646.47	0.00	17,681.82	0%	90%
DAM3-C-B11-E-14	Installation of Conduits and wiring outlets - Fire Alarm Syste	4	28-Oct-26	01-Nov-26	1,768.31	0.00	884.15	0%	50%
DAM3-C-B11-E-18	Installation of Sleeves & Power outlet	8	28-Oct-26	05-Nov-26	2,920.45	0.00	1,460.23	0%	50%
SITE INFRASTRUCTURE		56	07-Sep-26	10-Dec-26	1,157,556.84	531,245.38	1,025,101.05	45.89%	88.56%
NETWORKS		42	07-Sep-26	21-Oct-26	571,716.96	531,245.38	497,845.16	92.92%	87.08%
INTERNAL FIRE FIGHTING WATER SUPPLY SYSTEM (OUTSIDE BUILDING UI		42	07-Sep-26	21-Oct-26	571,716.96	531,245.38	497,845.16	92.92%	87.08%
DAM3-C-ENV-F-212	Excavation for External Fire Fighting Works	7	07-Sep-26	14-Sep-26	40,471.58	40,471.58	36,424.43	100%	90%
DAM3-C-ENV-F-172	Installation of HDPE PN16 Pipes (200 Dia)	10	15-Sep-26	27-Sep-26	364,244.28	364,244.28	327,819.85	100%	90%
DAM3-C-ENV-F-192	Installation of Valves	5	30-Sep-26	05-Oct-26	86,057.93	86,057.93	68,846.34	100%	80%
DAM3-C-ENV-F-202	Warning Tapes	2	28-Sep-26	29-Sep-26	40,471.58	40,471.58	32,377.27	100%	80%
DAM3-C-ENV-F-222	Backfilling for External Fire Fighting Works	14	06-Oct-26	21-Oct-26	40,471.58	0.00	32,377.27	0%	80%
EXTERNAL WORKS		10	30-Nov-26	10-Dec-26	585,839.88	0.00	527,255.89	0%	90%
MECHANICAL		10	30-Nov-26	10-Dec-26	585,839.88	0.00	527,255.89	0%	90%
DAM3-C-ENV-M-13	Installation of GRP Tanks	10	30-Nov-26	10-Dec-26	585,839.88	0.00	527,255.89	0%	90%
TESTING AND COMMISSIONING (10%)		7	24-May-26	03-Jun-26	63,346.56	63,346.56	47,509.92	100%	75%
TESTING AND COMMISSIONING 900 Sq.m-2		7	24-May-26	03-Jun-26	63,346.56	63,346.56	47,509.92	100%	75%
MECHANICAL		7	24-May-26	03-Jun-26	63,346.56	63,346.56	47,509.92	100%	75%
P001-C-TC-M-3406	Testing & Commissioning of Sewer & Drainage Pipes	7	24-May-26	03-Jun-26	63,346.56	63,346.56	47,509.92	100%	75%

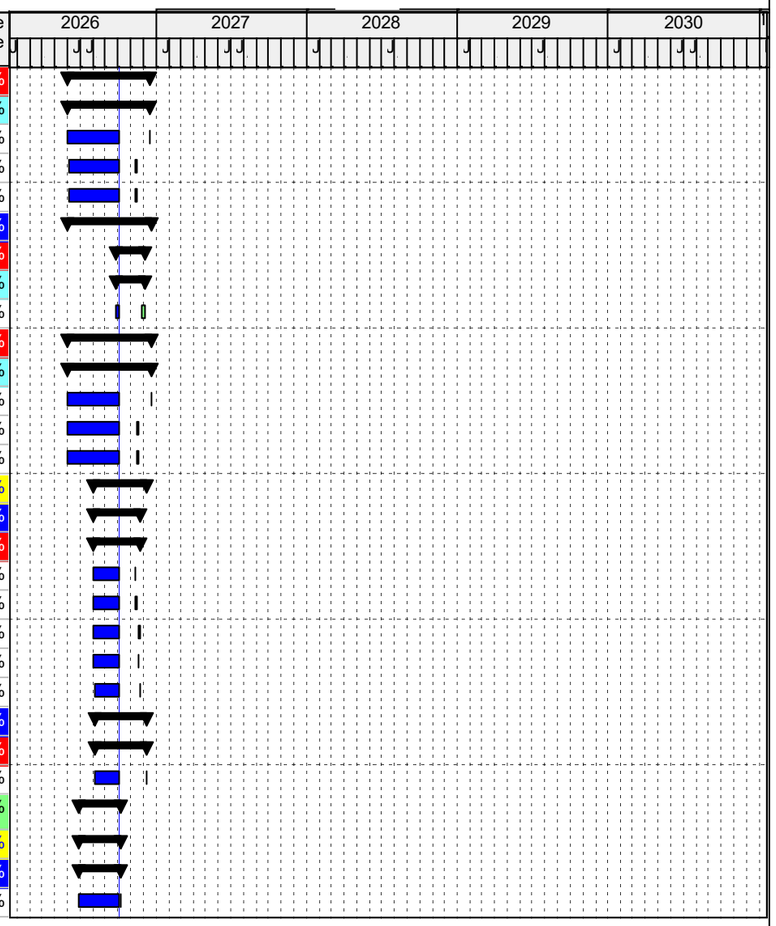

Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary

Date	Revision	Checked	Approved
06-Oct-25	2 Weeks look ahead		
