

Activity ID	Activity Name	BL Project Start	BL Project Finish	Actual Start	Finish	Performance % Complete
44 READY BUILT FACTORIES 900 m2 IN AL DAMMAM #3		20-May-26	05-Oct-26	16-May-26	07-Dec-26	80.55%
CONSTRUCTION (67%)		20-May-26	05-Oct-26	16-May-26	07-Dec-26	80.88%
RBF 900 SQM FACTORIES		20-May-26	05-Oct-26	16-May-26	07-Dec-26	74.09%
BLOCK B6		20-May-26	07-Jul-26	08-Jun-26	10-Oct-26	84.82%
ELECTRICAL		20-May-26	07-Jul-26	08-Jun-26	10-Oct-26	84.82%
FIRST STAGE		20-May-26	07-Jul-26	08-Jun-26	10-Oct-26	84.82%
DAM3-C-B6-E-343	Installation of Earthing and Grounding	04-Jul-26	07-Jul-26	08-Jun-26	06-Oct-26	90%
DAM3-C-B6-E-413	Installation of Sleeves & Power outlet	20-May-26	01-Jun-26	08-Jun-26	10-Oct-26	50%
BLOCK B5		22-Jun-26	05-Sep-26	04-Jun-26	22-Nov-26	87.59%
STRUCTURAL STEEL		22-Jun-26	27-Jun-26	04-Oct-26	06-Oct-26	90%
DAM3-C-B5-SS-300	Installation of wall sandwich panel	22-Jun-26	27-Jun-26	04-Oct-26	06-Oct-26	90%
ARCHITECTURAL		09-Jul-26	26-Jul-26	26-Sep-26	14-Oct-26	75%
WALL FINISHES		09-Jul-26	26-Jul-26	26-Sep-26	14-Oct-26	75%
DAM3-C-B5-A-145	Internal Wall Plaster	09-Jul-26	26-Jul-26	26-Sep-26	14-Oct-26	75%
ELECTRICAL		30-Jun-26	05-Sep-26	04-Jun-26	22-Nov-26	50%
FIRST STAGE		30-Jun-26	05-Sep-26	04-Jun-26	22-Nov-26	50%
DAM3-C-B5-E-833	Installation of Conduits and wiring outlets - Fire Alarm Syste	01-Sep-26	05-Sep-26	04-Jun-26	22-Nov-26	50%
DAM3-C-B5-E-873	Installation of Sleeves & Power outlet	30-Jun-26	08-Jul-26	04-Jun-26	10-Oct-26	50%
BLOCK B4		22-Jul-26	28-Sep-26	24-May-26	07-Dec-26	50%
ELECTRICAL		22-Jul-26	28-Sep-26	24-May-26	07-Dec-26	50%
FIRST STAGE		22-Jul-26	28-Sep-26	24-May-26	07-Dec-26	50%
DAM3-C-B4-E-603	Installation of Conduits and wiring outlets - Fire Alarm Syste	24-Sep-26	28-Sep-26	24-May-26	07-Dec-26	50%
DAM3-C-B4-E-643	Installation of Sleeves & Power outlet	22-Jul-26	30-Jul-26	24-May-26	26-Oct-26	50%
BLOCK B3		20-Jun-26	27-Jul-26	17-Jun-26	25-Oct-26	50%
STRUCTURAL		20-Jun-26	20-Jun-26	26-Sep-26	06-Oct-26	50%
COLUMNS & BEAMS		20-Jun-26	20-Jun-26	26-Sep-26	06-Oct-26	50%
DAM3-C-B3-S-613	Pouring Concrete for Beams	20-Jun-26	20-Jun-26	26-Sep-26	06-Oct-26	50%
ELECTRICAL		19-Jul-26	27-Jul-26	17-Jun-26	25-Oct-26	50%
FIRST STAGE		19-Jul-26	27-Jul-26	17-Jun-26	25-Oct-26	50%
DAM3-C-B3-E-643	Installation of Sleeves & Power outlet	19-Jul-26	27-Jul-26	17-Jun-26	25-Oct-26	50%
BLOCK B2		29-Sep-26	04-Oct-26	17-Jun-26	22-Nov-26	50%
ELECTRICAL		29-Sep-26	04-Oct-26	17-Jun-26	22-Nov-26	50%
FIRST STAGE		29-Sep-26	04-Oct-26	17-Jun-26	22-Nov-26	50%
DAM3-C-B2-E-143	Installation of Conduits and wiring outlets - Fire Alarm Syste	29-Sep-26	04-Oct-26	17-Jun-26	22-Nov-26	50%
BLOCK B7		24-Sep-26	05-Oct-26	16-May-26	26-Nov-26	26.19%
ARCHITECTURAL		24-Sep-26	01-Oct-26	05-Oct-26	26-Nov-26	25%
DOORS & WINDOWS		24-Sep-26	01-Oct-26	05-Oct-26	26-Nov-26	25%
DAM3-C-B7-A-552	Window (CW1)	24-Sep-26	01-Oct-26	05-Oct-26	26-Nov-26	25%
ELECTRICAL		27-Sep-26	05-Oct-26	16-May-26	16-Nov-26	50%
FIRST STAGE		27-Sep-26	05-Oct-26	16-May-26	16-Nov-26	50%
DAM3-C-B7-E-143	Installation of Conduits and wiring outlets - Fire Alarm Syste	27-Sep-26	30-Sep-26	16-May-26	14-Nov-26	50%
DAM3-C-B7-E-183	Installation of Sleeves & Power outlet	27-Sep-26	05-Oct-26	18-May-26	16-Nov-26	50%
SITE INFRASTRUCTURE		07-Sep-26	05-Oct-26	01-Aug-26	22-Nov-26	87.62%
NETWORKS		07-Sep-26	05-Oct-26	01-Aug-26	22-Nov-26	87.62%
INTERNAL FIRE FIGHTING WATER SUPPLY SYSTEM (OUTSIDE BUILDING UI		07-Sep-26	05-Oct-26	01-Aug-26	22-Nov-26	87.62%
DAM3-C-ENV-F-212	Excavation for External Fire Fighting Works	07-Sep-26	14-Sep-26	01-Aug-26	12-Nov-26	90%
DAM3-C-ENV-F-172	Installation of HDPE PN16 Pipes (200 Dia)	15-Sep-26	27-Sep-26	02-Aug-26	14-Nov-26	90%
DAM3-C-ENV-F-192	Installation of Valves	30-Sep-26	05-Oct-26	02-Aug-26	22-Nov-26	80%
DAM3-C-ENV-F-202	Warning Tapes	28-Sep-26	29-Sep-26	03-Aug-26	21-Nov-26	80%

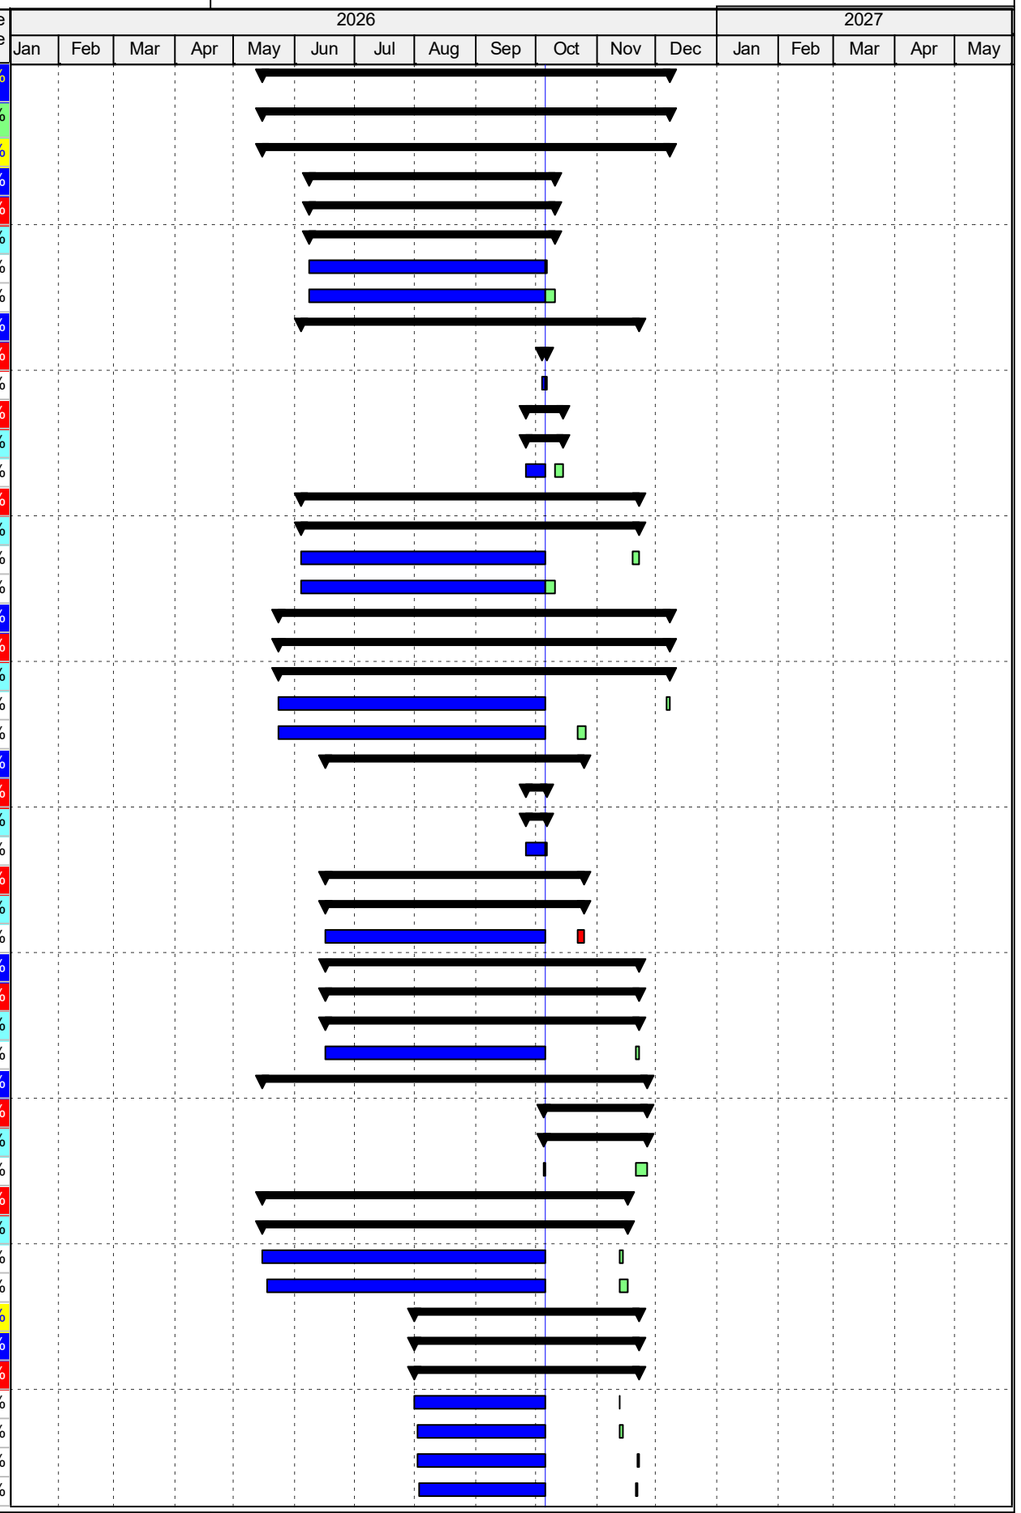

Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary

Date	Revision	Checked	Approved
06-Oct-26	Critical Activities	OA	

Activity ID	Activity Name	BL Project Start	BL Project Finish	Actual Start	Finish	Performance % Complete
TESTING AND COMMISSIONING (10%)		24-May-26	03-Jun-26	28-Jun-26	07-Oct-26	75%
TESTING AND COMMISSIONING 900 Sq.m-2		24-May-26	03-Jun-26	28-Jun-26	07-Oct-26	75%
MECHANICAL		24-May-26	03-Jun-26	28-Jun-26	07-Oct-26	75%
P001-C-TC-M-3406	Testing & Commissioning of Sewer & Drainage Pipes	24-May-26	03-Jun-26	28-Jun-26	07-Oct-26	75%



Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary

Date	Revision	Checked	Approved
06-Oct-26	Critical Activities	OA	
