

Activity ID	Activity Name	Original Duration	BL Project Start	BL Project Finish	Start	Finish	Budgeted Total Cost	Planned Value Cost	Earned Value Cost	Schedule % Complete	Performance % Complete
44 READY BUILT FACTORIES 900 m2 IN AL DAMMAM #3		366	07-Jan-26	06-Mar-27	07-Jan-26 A	06-Mar-27	95,996,525.00	65,605,417.65	65,630,825.45	68.34%	68.37%
PROJECT MILESTONES		353	07-Jan-26	06-Mar-27	07-Jan-26 A	06-Mar-27	0.00	0.00	0.00	0%	0%
CONTRACTUAL MILESTONES		353	07-Jan-26	06-Mar-27	07-Jan-26 A	06-Mar-27	0.00	0.00	0.00	0%	0%
DAM3-PMS-MMS-0010	Project Start Date	0	07-Jan-26		07-Jan-26 A		0.00	0.00	0.00	100%	100%
DAM3-PMS-MMS-0020	Completion of Mobilization Works	0		07-Feb-26		18-Jan-26 A	0.00	0.00	0.00	100%	100%
DAM3-PMS-MMS-0040	Completion of Time Schedule submission	0		28-Jan-26		11-Feb-26 A	0.00	0.00	0.00	100%	100%
DAM3-PMS-MMS-0030	Completion of Site Suvey Works	0		09-Feb-26		12-Feb-26 A	0.00	0.00	0.00	100%	100%
DAM3-PMS-MMS-0050	Completion of Plans (PEP,PQP,HSE, Procurement Plan)	0		04-Feb-26		04-May-26 A	0.00	0.00	0.00	100%	100%
DAM3-PMS-MMS-0060	Completion of Engineering and Materials	0		07-May-26		05-Jul-26 A	0.00	0.00	0.00	100%	100%
DAM3-PMS-MMS-0080	Network start	0	07-Sep-26		01-Aug-26 A		0.00	0.00	0.00	100%	100%
DAM3-PMS-MMS-0070	Completion of Site levelling, local roads & parkings	0		12-Feb-26		06-Oct-26	0.00	0.00	0.00	100%	0%
DAM3-PMS-MMS-0110	Competion of Testing and Commissioning	0		06-Feb-27		04-Jan-27	0.00	0.00	0.00	0%	0%
DAM3-PMS-MMS-0090	Completion of Construction	0		21-Feb-27		25-Feb-27	0.00	0.00	0.00	0%	0%
DAM3-PMS-MMS-0100	Project Completion Date	0		06-Mar-27		06-Mar-27	0.00	0.00	0.00	0%	0%
DISCIPLINE MILESTONES		294	27-Jan-26	21-Feb-27	15-Feb-26 A	25-Feb-27	0.00	0.00	0.00	0%	0%
900 SQM FACTORIES		294	27-Jan-26	21-Feb-27	15-Feb-26 A	25-Feb-27	0.00	0.00	0.00	0%	0%
DAM3-PMS-DMS-2360	Construction Start	0	27-Jan-26		15-Feb-26 A		0.00	0.00	0.00	100%	100%
DAM3-PMS-DMS-2310	Completion of Civil works	0		01-Oct-26		03-Dec-26	0.00	0.00	0.00	100%	0%
DAM3-PMS-DMS-2330	Completion of Mechanical works	0		14-Dec-26		30-Jan-27	0.00	0.00	0.00	0%	0%
DAM3-PMS-DMS-2320	Completion of Electrical works	0		21-Dec-26		13-Feb-27	0.00	0.00	0.00	0%	0%
DAM3-PMS-DMS-2340	Completion of Architectural works	0		21-Dec-26		13-Feb-27	0.00	0.00	0.00	0%	0%
DAM3-PMS-DMS-2370	Construction Finish	0		21-Feb-27		25-Feb-27	0.00	0.00	0.00	0%	0%
SITE INFRASTRUCTURE		20	22-Dec-26	21-Feb-27	01-Feb-27	25-Feb-27	0.00	0.00	0.00	0%	0%
DAM3-PMS-DMS-2460	Completion of Environmentall works	0		22-Dec-26		01-Feb-27	0.00	0.00	0.00	0%	0%
DAM3-PMS-DMS-2450	Completion of External works	0		21-Feb-27		25-Feb-27	0.00	0.00	0.00	0%	0%
MOBILIZATION		35	07-Jan-26	16-Feb-26	07-Jan-26 A	04-May-26 A	0.00	0.00	0.00	0%	0%
SITE FACILITIES AND OFFICES		27	07-Jan-26	07-Feb-26	07-Jan-26 A	23-Feb-26 A	0.00	0.00	0.00	0%	0%
DAM3-MOB-SO.0019	Mobilization of Manpower	2	05-Feb-26	07-Feb-26	07-Jan-26 A	23-Feb-26 A	0.00	0.00	0.00	100%	100%
DAM3-MOB-SO.0014	Clear and Grub for Offices and Access Roads	2	15-Jan-26	17-Jan-26	11-Jan-26 A	16-Feb-26 A	0.00	0.00	0.00	100%	100%
DAM3-MOB-SO.0015	Construct Site Offices	4	18-Jan-26	21-Jan-26	19-Jan-26 A	10-Feb-26 A	0.00	0.00	0.00	100%	100%
DAM3-MOB-SO.0020	Mobilization of Equipment	2	05-Feb-26	07-Feb-26	25-Jan-26 A	23-Feb-26 A	0.00	0.00	0.00	100%	100%
DAM3-MOB-SO.0018	Install Project Signs	4	01-Feb-26	04-Feb-26	03-Feb-26 A	04-Feb-26 A	0.00	0.00	0.00	100%	100%
DAM3-MOB-SO.0011	Site Layout Plan Prep	2	10-Jan-26	11-Jan-26	04-Feb-26 A	04-Feb-26 A	0.00	0.00	0.00	100%	100%
DAM3-MOB-SO.0012	Site Layout Plan Submittal	2	12-Jan-26	13-Jan-26	04-Feb-26 A	04-Feb-26 A	0.00	0.00	0.00	100%	100%
DAM3-MOB-SO.0013	Site Layout Plan Owner Approval	2	14-Jan-26	15-Jan-26	04-Feb-26 A	16-Feb-26 A	0.00	0.00	0.00	100%	100%
DAM3-MOB-SO.0016	Electrical Works and Connections	4	22-Jan-26	26-Jan-26	09-Feb-26 A	23-Feb-26 A	0.00	0.00	0.00	100%	100%
DAM3-MOB-SO.0017	Site Utilities	4	27-Jan-26	31-Jan-26	11-Feb-26 A	23-Feb-26 A	0.00	0.00	0.00	100%	100%
DAM3-MOB-SO.0010	Site Survey	2	07-Jan-26	08-Jan-26	12-Feb-26 A	12-Feb-26 A	0.00	0.00	0.00	100%	100%
PRELIMINARY SUBMITTALS		31	22-Jan-26	16-Feb-26	14-Jan-26 A	04-May-26 A	0.00	0.00	0.00	0%	0%
PREPARATION AND SUBMITTALS		21	22-Jan-26	04-Feb-26	14-Jan-26 A	21-Feb-26 A	0.00	0.00	0.00	0%	0%
DAM3-PRE-SUB-0012	Baseline Schedule	2	27-Jan-26	28-Jan-26	14-Jan-26 A	14-Jan-26 A	0.00	0.00	0.00	100%	100%
DAM3-PRE-SUB-0011	Health & Safety Plan	2	25-Jan-26	26-Jan-26	26-Jan-26 A	26-Jan-26 A	0.00	0.00	0.00	100%	100%
DAM3-PRE-SUB-0015	Quality Control Plan	2	03-Feb-26	04-Feb-26	28-Jan-26 A	28-Jan-26 A	0.00	0.00	0.00	100%	100%
DAM3-PRE-SUB-0013	Risk Management plan	2	29-Jan-26	31-Jan-26	28-Jan-26 A	28-Jan-26 A	0.00	0.00	0.00	100%	100%
DAM3-PRE-SUB-0014	Communication Plan	2	01-Feb-26	02-Feb-26	21-Feb-26 A	21-Feb-26 A	0.00	0.00	0.00	100%	100%
DAM3-PRE-SUB-0010	Project Execution Plan	2	22-Jan-26	24-Jan-26	21-Feb-26 A	21-Feb-26 A	0.00	0.00	0.00	100%	100%
REVIEW AND APPROVALS		29	25-Jan-26	16-Feb-26	14-Jan-26 A	04-May-26 A	0.00	0.00	0.00	0%	0%
DAM3-PRE-SUB-1015	Baseline Schedule	10	05-Feb-26	16-Feb-26	14-Jan-26 A	10-Feb-26 A	0.00	0.00	0.00	100%	100%

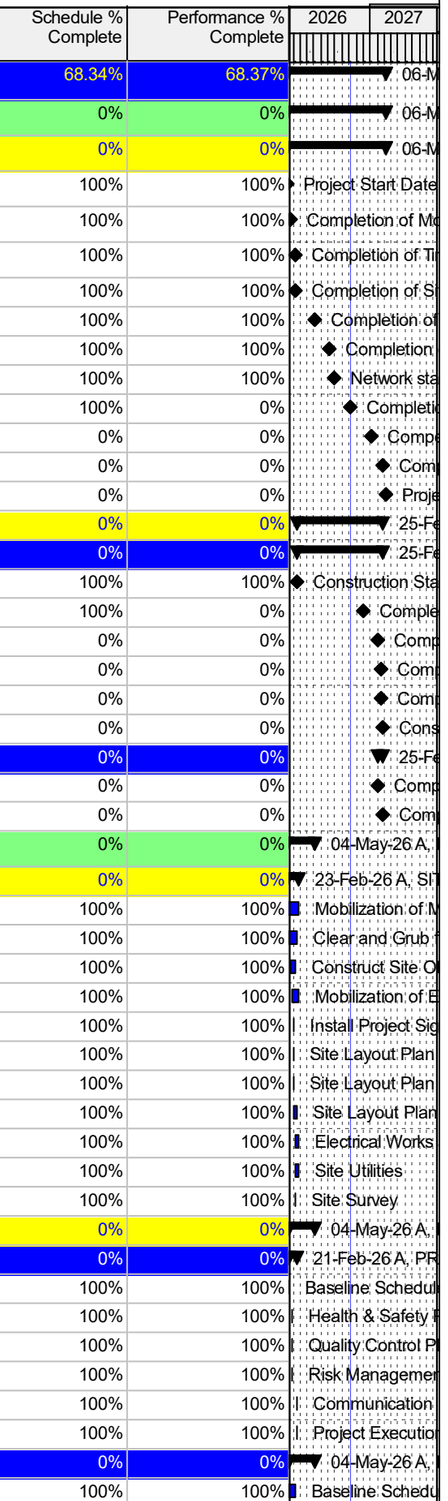

Actual Level of Effort | Remaining Work | Milestone
Actual Work | Critical Remaining Work | summary

Date	Revision	Checked	Approved
06-Oct-26	Weekly Report		

Activity ID	Activity Name	Original Duration	BL Project Start	BL Project Finish	Start	Finish	Budgeted Total Cost	Planned Value Cost	Earned Value Cost	Schedule % Complete	Performance % Complete
DAM3-PRE-SUB-1011	Health & Safety Plan	10	27-Jan-26	07-Feb-26	26-Jan-26 A	28-Jan-26 A	0.00	0.00	0.00	100%	100%
DAM3-PRE-SUB-1014	Quality Control Plan	10	05-Feb-26	16-Feb-26	28-Jan-26 A	04-May-26 A	0.00	0.00	0.00	100%	100%
DAM3-PRE-SUB-1012	Risk Management plan	10	01-Feb-26	11-Feb-26	28-Jan-26 A	03-Feb-26 A	0.00	0.00	0.00	100%	100%
DAM3-PRE-SUB-1013	Communication Plan	10	03-Feb-26	14-Feb-26	21-Feb-26 A	03-May-26 A	0.00	0.00	0.00	100%	100%
DAM3-PRE-SUB-1010	Project Execution Plan	10	25-Jan-26	04-Feb-26	21-Feb-26 A	03-May-26 A	0.00	0.00	0.00	100%	100%
ENGINEERING (3%)		159	22-Jan-26	17-May-26	15-Jan-26 A	05-Jul-26 A	2,879,895.75	2,879,895.75	2,879,895.75	100%	100%
SHOP DRAWINGS		138	27-Jan-26	17-May-26	20-Jan-26 A	05-Jul-26 A	0.00	0.00	0.00	0%	0%
PREPARATION AND SUBMITTAL		136	27-Jan-26	07-May-26	20-Jan-26 A	01-Jul-26 A	0.00	0.00	0.00	0%	0%
STRUCTURAL		87	10-Feb-26	22-Mar-26	03-Feb-26 A	02-Jun-26 A	0.00	0.00	0.00	0%	0%
DAM3-E-SS-C-830	SECTIONS	2	03-Mar-26	04-Mar-26	03-Feb-26 A	03-Feb-26 A	0.00	0.00	0.00	100%	100%
DAM3-E-SS-C-840	EXTERNAL WALL SECTION DETAILS	2	05-Mar-26	07-Mar-26	03-Feb-26 A	03-Feb-26 A	0.00	0.00	0.00	100%	100%
DAM3-E-SS-C-850	BASE PLATE DETAILS	2	08-Mar-26	09-Mar-26	03-Feb-26 A	03-Feb-26 A	0.00	0.00	0.00	100%	100%
DAM3-E-SS-C-770	BASE PLATE LAYOUT	2	15-Feb-26	16-Feb-26	07-Feb-26 A	07-Feb-26 A	0.00	0.00	0.00	100%	100%
DAM3-E-SS-C-790	ROOF FRAMING LAYOUT	2	19-Feb-26	23-Feb-26	07-Feb-26 A	07-Feb-26 A	0.00	0.00	0.00	100%	100%
DAM3-E-SS-C-800	PURLINS FRAMING LAYOUT	2	23-Feb-26	25-Feb-26	07-Feb-26 A	07-Feb-26 A	0.00	0.00	0.00	100%	100%
DAM3-E-SS-C-810	ROOF SHEETING LAYOUT	2	25-Feb-26	28-Feb-26	07-Feb-26 A	07-Feb-26 A	0.00	0.00	0.00	100%	100%
DAM3-E-SS-C-820	COLUMNS AND AXIS LAYOUT	2	01-Mar-26	02-Mar-26	07-Feb-26 A	07-Feb-26 A	0.00	0.00	0.00	100%	100%
DAM3-E-SS-C-750	FOUNDATION LAYOUT	2	10-Feb-26	11-Feb-26	18-Feb-26 A	18-Feb-26 A	0.00	0.00	0.00	100%	100%
DAM3-E-SS-C-780	TIE BEAM @ 4500mm EL.	2	17-Feb-26	19-Feb-26	01-Mar-26 A	01-Mar-26 A	0.00	0.00	0.00	100%	100%
DAM3-E-SS-C-880	PUMP SHED AND GRP WATER TANK STRUCTURAL DETAILS (1-2)	2	15-Mar-26	16-Mar-26	29-Mar-26 A	29-Mar-26 A	0.00	0.00	0.00	100%	100%
DAM3-E-SS-C-890	PUMP SHED AND GRP WATER TANK STRUCTURAL DETAILS (2-2)	2	21-Mar-26	22-Mar-26	29-Mar-26 A	29-Mar-26 A	0.00	0.00	0.00	100%	100%
DAM3-E-SS-C-760	GRADE BEAM / SLAB ON GRADE LAYOUT	2	12-Feb-26	14-Feb-26	21-Apr-26 A	21-Apr-26 A	0.00	0.00	0.00	100%	100%
DAM3-E-SS-C-860	TYPICAL STRUCTURAL SECTION DETAILS	2	10-Mar-26	11-Mar-26	21-Apr-26 A	21-Apr-26 A	0.00	0.00	0.00	100%	100%
DAM3-E-SS-C-870	STRUCTURAL SCHEDULE	2	12-Mar-26	14-Mar-26	02-Jun-26 A	02-Jun-26 A	0.00	0.00	0.00	100%	100%
ARCHITECTURAL		75	25-Feb-26	04-Apr-26	03-Feb-26 A	02-Jun-26 A	0.00	0.00	0.00	0%	0%
DAM3-E-SS-A-830	GROUND FLOOR LAYOUT PLAN	2	25-Feb-26	28-Feb-26	03-Feb-26 A	03-Feb-26 A	0.00	0.00	0.00	100%	100%
DAM3-E-SS-A-840	GROUND FLOOR ENLARGED LAYOUT PLAN	2	01-Mar-26	02-Mar-26	03-Feb-26 A	03-Feb-26 A	0.00	0.00	0.00	100%	100%
DAM3-E-SS-A-860	ELEVATIONS (SHEET 01 0F 02)	2	05-Mar-26	07-Mar-26	03-Feb-26 A	03-Feb-26 A	0.00	0.00	0.00	100%	100%
DAM3-E-SS-A-870	BUILDING SECTIONS	2	08-Mar-26	09-Mar-26	03-Feb-26 A	03-Feb-26 A	0.00	0.00	0.00	100%	100%
DAM3-E-SS-A-880	WALL SECTIONS	2	11-Mar-26	12-Mar-26	03-Feb-26 A	03-Feb-26 A	0.00	0.00	0.00	100%	100%
DAM3-E-SS-A-1170	ELEVATIONS (SHEET 01 0F 02)	5	05-Mar-26	10-Mar-26	03-Feb-26 A	03-Feb-26 A	0.00	0.00	0.00	100%	100%
DAM3-E-SS-A-890	CEILING LAYOUT PLAN	2	14-Mar-26	15-Mar-26	05-Feb-26 A	05-Feb-26 A	0.00	0.00	0.00	100%	100%
DAM3-E-SS-A-900	FINISHING LAYOUT PLAN	2	16-Mar-26	21-Mar-26	09-Feb-26 A	09-Feb-26 A	0.00	0.00	0.00	100%	100%
DAM3-E-SS-A-910	TOILET DETAILS	2	22-Mar-26	23-Mar-26	11-Feb-26 A	11-Feb-26 A	0.00	0.00	0.00	100%	100%
DAM3-E-SS-A-920	DOORS & WINDOWS SCHEDULE	2	24-Mar-26	25-Mar-26	11-Feb-26 A	11-Feb-26 A	0.00	0.00	0.00	100%	100%
DAM3-E-SS-A-930	MISCELLANEOUS DETAILS - 01	2	26-Mar-26	28-Mar-26	11-Feb-26 A	11-Feb-26 A	0.00	0.00	0.00	100%	100%
DAM3-E-SS-A-940	MISCELLANEOUS DETAILS - 02	2	29-Mar-26	30-Mar-26	11-Feb-26 A	11-Feb-26 A	0.00	0.00	0.00	100%	100%
DAM3-E-SS-A-950	SIGNAGE LOCATION PLAN	2	31-Mar-26	01-Apr-26	11-Feb-26 A	11-Feb-26 A	0.00	0.00	0.00	100%	100%
DAM3-E-SS-A-960	SIGNAGE DESIGN DETAILS	2	02-Apr-26	04-Apr-26	11-Feb-26 A	11-Feb-26 A	0.00	0.00	0.00	100%	100%
DAM3-E-SS-A-850	SKYLIGHT DISTRIBUTION - ROOF LAYOUT PLAN	2	03-Mar-26	04-Mar-26	02-Jun-26 A	02-Jun-26 A	0.00	0.00	0.00	100%	100%
MECHANICAL		47	03-Mar-26	23-Apr-26	04-Feb-26 A	16-Apr-26 A	0.00	0.00	0.00	0%	0%
DAM3-E-SS-M-650	SCHEMATIC RISER DIAGRAM PLUMBING-DRAINAGE	2	15-Mar-26	16-Mar-26	04-Feb-26 A	04-Feb-26 A	0.00	0.00	0.00	100%	100%
DAM3-E-SS-M-660	SCHEMATIC RISER DIAGRAM PLUMBING-WATER	2	21-Mar-26	22-Mar-26	04-Feb-26 A	04-Feb-26 A	0.00	0.00	0.00	100%	100%
DAM3-E-SS-M-670	GENERAL MISELLANEOUS DETAILS PLUMBING	2	23-Mar-26	24-Mar-26	04-Feb-26 A	04-Feb-26 A	0.00	0.00	0.00	100%	100%
DAM3-E-SS-M-680	GENERAL MISELLANEOUS DETAILS PLUMBING	2	25-Mar-26	26-Mar-26	04-Feb-26 A	04-Feb-26 A	0.00	0.00	0.00	100%	100%
DAM3-E-SS-M-750	GENERAL-INSTRUMENTATION & CONTROL	2	11-Apr-26	12-Apr-26	04-Feb-26 A	04-Feb-26 A	0.00	0.00	0.00	100%	100%
DAM3-E-SS-M-780	SCHEMATIC RISER DIAGRAM FIREFIGHTING	2	18-Apr-26	19-Apr-26	04-Feb-26 A	04-Feb-26 A	0.00	0.00	0.00	100%	100%
DAM3-E-SS-M-790	GENERAL-MISCELLANEOUS DETAILS- FIRE FIGHTING	2	20-Apr-26	21-Apr-26	04-Feb-26 A	04-Feb-26 A	0.00	0.00	0.00	100%	100%
DAM3-E-SS-M-800	MISCELLANEOUS DETAILS	2	22-Apr-26	23-Apr-26	04-Feb-26 A	04-Feb-26 A	0.00	0.00	0.00	100%	100%



Actual Level of Effort | Remaining Work | Milestone
Actual Work | Critical Remaining Work | summary

Date	Revision	Checked	Approved
06-Oct-26	Weekly Report		

Activity ID	Activity Name	Original Duration	BL Project Start	BL Project Finish	Start	Finish	Budgeted Total Cost	Planned Value Cost	Earned Value Cost	Schedule % Complete	Performance % Complete	2026 2027
DAM3-E-SS-M-760	GENERAL MISCELLANEOUS DETAILS - HVAC	2	13-Apr-26	14-Apr-26	05-Feb-26 A	05-Feb-26 A	0.00	0.00	0.00	100%	100%	GENERAL MISC
DAM3-E-SS-M-610	TOILETS DETAILS PLUMBING-DRAINAGE	2	05-Mar-26	07-Mar-26	11-Mar-26 A	11-Mar-26 A	0.00	0.00	0.00	100%	100%	TOILETS DETA
DAM3-E-SS-M-640	TOILET DETAILS PLUMBING-WATER	2	12-Mar-26	14-Mar-26	11-Mar-26 A	11-Mar-26 A	0.00	0.00	0.00	100%	100%	TOILET DETAIL
DAM3-E-SS-M-770	TYPICAL GROUND FLOOR PLAN FIREFIGHTING	2	15-Apr-26	16-Apr-26	14-Mar-26 A	14-Mar-26 A	0.00	0.00	0.00	100%	100%	TYPICAL GROU
DAM3-E-SS-M-620	TYPICAL ROOF PLUMBING PLAN	2	08-Mar-26	09-Mar-26	16-Mar-26 A	16-Mar-26 A	0.00	0.00	0.00	100%	100%	TYPICAL ROOF
DAM3-E-SS-M-600	TYPICAL GROUND FLOOR PLAN-PLUMBING- DRAINAGE	2	03-Mar-26	04-Mar-26	17-Mar-26 A	17-Mar-26 A	0.00	0.00	0.00	100%	100%	TYPICAL GROU
DAM3-E-SS-M-630	GROUND FLOOR WATER SUPPLY PLAN	2	10-Mar-26	11-Mar-26	17-Mar-26 A	17-Mar-26 A	0.00	0.00	0.00	100%	100%	GROUND FLO
DAM3-E-SS-M-690	SCHEDULE- PLUMBING	2	28-Mar-26	29-Mar-26	17-Mar-26 A	17-Mar-26 A	0.00	0.00	0.00	100%	100%	SCHEDULE- P
DAM3-E-SS-M-720	SCHEDULES	2	04-Apr-26	05-Apr-26	17-Mar-26 A	17-Mar-26 A	0.00	0.00	0.00	100%	100%	SCHEDULES
DAM3-E-SS-M-730	GROUND FLOOR PLAN-HVAC SYSTEM	2	06-Apr-26	07-Apr-26	26-Mar-26 A	26-Mar-26 A	0.00	0.00	0.00	100%	100%	GROUND FLO
DAM3-E-SS-M-740	TYPICAL ROOF HVAC PLAN	2	08-Apr-26	09-Apr-26	26-Mar-26 A	26-Mar-26 A	0.00	0.00	0.00	100%	100%	TYPICAL ROO
DAM3-E-SS-M-700	PUMP ROOM LAYOUT	2	30-Mar-26	31-Mar-26	16-Apr-26 A	16-Apr-26 A	0.00	0.00	0.00	100%	100%	PUMP ROOM
DAM3-E-SS-M-710	PUMP ROOM 3D & SECTIONS VIEW	2	01-Apr-26	02-Apr-26	16-Apr-26 A	16-Apr-26 A	0.00	0.00	0.00	100%	100%	PUMP ROOM
ELECTRICAL		133	05-Mar-26	05-May-26	09-Feb-26 A	25-Jun-26 A	0.00	0.00	0.00	0%	0%	25-Jun-26 A
DAM3-E-SS-E-940	GROUND FLOOR POWER PLAN	2	05-Mar-26	07-Mar-26	09-Feb-26 A	09-Feb-26 A	0.00	0.00	0.00	100%	100%	GROUND FLOO
DAM3-E-SS-E-950	GROUND FLOOR POWER FOR MECHANICAL	2	08-Mar-26	09-Mar-26	09-Feb-26 A	09-Feb-26 A	0.00	0.00	0.00	100%	100%	GROUND FLOO
DAM3-E-SS-E-960	ROOF FLOOR POWER FOR MECHANICAL	2	10-Mar-26	11-Mar-26	09-Feb-26 A	09-Feb-26 A	0.00	0.00	0.00	100%	100%	ROOF FLOOR P
DAM3-E-SS-E-990	GROUND FLOOR LIGHTING PLAN	2	21-Mar-26	22-Mar-26	09-Feb-26 A	09-Feb-26 A	0.00	0.00	0.00	100%	100%	GROUND FLOO
DAM3-E-SS-E-1000	ROOF FLOOR LIGHTING PLAN	2	23-Mar-26	24-Mar-26	09-Feb-26 A	09-Feb-26 A	0.00	0.00	0.00	100%	100%	ROOF FLOOR L
DAM3-E-SS-E-1060	ROOF FLOOR LIGHTENING PLAN	2	06-Apr-26	07-Apr-26	09-Feb-26 A	09-Feb-26 A	0.00	0.00	0.00	100%	100%	ROOF FLOOR L
DAM3-E-SS-E-1140	POWER FOR MECHANICAL	2	25-Apr-26	26-Apr-26	09-Feb-26 A	09-Feb-26 A	0.00	0.00	0.00	100%	100%	POWER FOR M
DAM3-E-SS-E-1150	GROUND FLOOR LIGHTING PLAN	2	27-Apr-26	28-Apr-26	09-Feb-26 A	09-Feb-26 A	0.00	0.00	0.00	100%	100%	GROUND FLOO
DAM3-E-SS-E-1130	GROUND FLOOR POWER PLAN	1	22-Apr-26	23-Apr-26	09-Feb-26 A	09-Feb-26 A	0.00	0.00	0.00	100%	100%	GROUND FLOO
DAM3-E-SS-E-1030	GROUND FLOOR CCTV PLAN	2	30-Mar-26	31-Mar-26	01-Mar-26 A	01-Mar-26 A	0.00	0.00	0.00	100%	100%	GROUND FLOO
DAM3-E-SS-E-1040	GROUND FLOOR DATA & TELECOM PLAN	2	01-Apr-26	02-Apr-26	01-Mar-26 A	01-Mar-26 A	0.00	0.00	0.00	100%	100%	GROUND FLOO
DAM3-E-SS-E-1050	GROUND FLOOR GROUNDING PLAN	2	04-Apr-26	05-Apr-26	01-Mar-26 A	01-Mar-26 A	0.00	0.00	0.00	100%	100%	GROUND FLOO
DAM3-E-SS-E-1120	ELECTRICAL DETAILS	2	20-Apr-26	21-Apr-26	01-Mar-26 A	01-Mar-26 A	0.00	0.00	0.00	100%	100%	ELECTRICAL D
DAM3-E-SS-E-1160	GROUND FLOOR GROUNDING PLAN	2	29-Apr-26	30-Apr-26	01-Mar-26 A	01-Mar-26 A	0.00	0.00	0.00	100%	100%	GROUND FLOO
DAM3-E-SS-E-1180	ELECTRICAL DETAILS	2	04-May-26	05-May-26	01-Mar-26 A	01-Mar-26 A	0.00	0.00	0.00	100%	100%	ELECTRICAL D
DAM3-E-SS-E-1010	GOUND FLOOR ACCESS CONTROL	2	25-Mar-26	26-Mar-26	29-Mar-26 A	29-Mar-26 A	0.00	0.00	0.00	100%	100%	GOUND FLOO
DAM3-E-SS-E-1020	GROUND FLOOR FIRE ALARM PLAN	2	28-Mar-26	29-Mar-26	29-Mar-26 A	29-Mar-26 A	0.00	0.00	0.00	100%	100%	GROUND FLO
DAM3-E-SS-E-1070	POWER RISER DIAGRAM	2	08-Apr-26	09-Apr-26	29-Mar-26 A	29-Mar-26 A	0.00	0.00	0.00	100%	100%	POWER RISER
DAM3-E-SS-E-1080	FIRE ALARM RISER DIAGRAM	2	11-Apr-26	12-Apr-26	29-Mar-26 A	29-Mar-26 A	0.00	0.00	0.00	100%	100%	FIRE ALARM R
DAM3-E-SS-E-1090	DATA & TELECOME RISER DIAGRAM	2	13-Apr-26	14-Apr-26	29-Mar-26 A	29-Mar-26 A	0.00	0.00	0.00	100%	100%	DATA & TELEC
DAM3-E-SS-E-1100	ACCESS CONTROL RISER DIAGRAM	2	15-Apr-26	16-Apr-26	29-Mar-26 A	29-Mar-26 A	0.00	0.00	0.00	100%	100%	ACCESS CON
DAM3-E-SS-E-1110	SCHEDULES	2	18-Apr-26	19-Apr-26	29-Mar-26 A	29-Mar-26 A	0.00	0.00	0.00	100%	100%	SCHEDULES
DAM3-E-SS-E-970	ROOF FLOOR POWER	2	12-Mar-26	14-Mar-26	08-Apr-26 A	09-Apr-26 A	0.00	0.00	0.00	100%	100%	ROOF FLOOR
DAM3-E-SS-E-1170	RISER DIAGRAM	2	02-May-26	03-May-26	27-Apr-26 A	27-Apr-26 A	0.00	0.00	0.00	100%	100%	RISER DIAGR
DAM3-E-SS-E-980	PV SYSTEM CALCULATION	2	15-Mar-26	16-Mar-26	25-Jun-26 A	25-Jun-26 A	0.00	0.00	0.00	100%	100%	PV SYSTEM
ROAD DRAWINGS		117	27-Jan-26	29-Mar-26	20-Jan-26 A	01-Jul-26 A	0.00	0.00	0.00	0%	0%	01-Jul-26 A
DAM3-E-SS-R-780	TOPOGRAPHIC SURVEY-CONTOURS MAP	2	08-Feb-26	09-Feb-26	20-Jan-26 A	20-Jan-26 A	0.00	0.00	0.00	100%	100%	TOPOGRAPHIC
DAM3-E-SS-R-730	GRADING LAYOUT PLAN	2	27-Jan-26	28-Jan-26	03-Feb-26 A	03-Feb-26 A	0.00	0.00	0.00	100%	100%	GRADING LAYO
DAM3-E-SS-R-880	GENERAL SITE PLAN - OVERALL	2	05-Mar-26	07-Mar-26	08-Mar-26 A	08-Mar-26 A	0.00	0.00	0.00	100%	100%	GENERAL SITE
DAM3-E-SS-R-890	SITE SETTING-OUT PLAN - OVERALL	2	08-Mar-26	09-Mar-26	08-Mar-26 A	08-Mar-26 A	0.00	0.00	0.00	100%	100%	SITE SETTING-
DAM3-E-SS-R-900	GENERAL LANDSCAPE LAYOUT	2	10-Mar-26	11-Mar-26	08-Mar-26 A	08-Mar-26 A	0.00	0.00	0.00	100%	100%	GENERAL LAN
DAM3-E-SS-R-910	GENERAL HARDSCAPE LAYOUT	2	12-Mar-26	14-Mar-26	08-Mar-26 A	08-Mar-26 A	0.00	0.00	0.00	100%	100%	GENERAL HAR
DAM3-E-SS-R-920	GENERAL SOFTSCAPE LAYOUT	2	15-Mar-26	16-Mar-26	08-Mar-26 A	08-Mar-26 A	0.00	0.00	0.00	100%	100%	GENERAL SOF
DAM3-E-SS-R-960	LANDSCAPE SCHEDULES	2	28-Mar-26	29-Mar-26	08-Mar-26 A	08-Mar-26 A	0.00	0.00	0.00	100%	100%	LANDSCAPE S
DAM3-E-SS-R-930	PUMP ROOM DETAILS	1	21-Mar-26	22-Mar-26	14-Mar-26 A	14-Mar-26 A	0.00	0.00	0.00	100%	100%	PUMP ROOM D

Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary

Date	Revision	Checked	Approved
06-Oct-26	Weekly Report		

Activity ID	Activity Name	Original Duration	BL Project Start	BL Project Finish	Start	Finish	Budgeted Total Cost	Planned Value Cost	Earned Value Cost	Schedule % Complete	Performance % Complete	2026	2027
DAM3-E-SS-R-740	ROAD LAYOUT PLAN	2	29-Jan-26	31-Jan-26	16-Mar-26 A	16-Mar-26 A	0.00	0.00	0.00	100%	100%	ROAD LAYOUT	
DAM3-E-SS-R-750	TYPICAL CROSS SECTIONS - KEY PLAN	2	01-Feb-26	02-Feb-26	16-Mar-26 A	16-Mar-26 A	0.00	0.00	0.00	100%	100%	TYPICAL CROS	
DAM3-E-SS-R-760	TYPICAL CROSS SECTIONS	2	03-Feb-26	04-Feb-26	16-Mar-26 A	16-Mar-26 A	0.00	0.00	0.00	100%	100%	TYPICAL CROS	
DAM3-E-SS-R-770	ROAD PROFILES	2	05-Feb-26	07-Feb-26	16-Mar-26 A	16-Mar-26 A	0.00	0.00	0.00	100%	100%	ROAD PROFIL	
DAM3-E-SS-R-940	GENERAL DETAILS	1	23-Mar-26	24-Mar-26	18-Mar-26 A	18-Mar-26 A	0.00	0.00	0.00	100%	100%	GENERAL DET	
DAM3-E-SS-R-830	SIGNING & MARKING LAYOUT PLAN	2	19-Feb-26	23-Feb-26	21-Apr-26 A	21-Apr-26 A	0.00	0.00	0.00	100%	100%	SIGNING & M	
DAM3-E-SS-R-840	ROAD STANDARD DETAILS-TYPICAL PAVEMENT DETAILS	2	23-Feb-26	25-Feb-26	21-Apr-26 A	21-Apr-26 A	0.00	0.00	0.00	100%	100%	ROAD STAND	
DAM3-E-SS-R-850	ROAD STANDARD DETAILS-TYPICAL CURB DETAILS	2	25-Feb-26	28-Feb-26	21-Apr-26 A	21-Apr-26 A	0.00	0.00	0.00	100%	100%	ROAD STAND	
DAM3-E-SS-R-860	ROAD STANDARD DETAILS-ROAD SIGN DETAILS	2	01-Mar-26	02-Mar-26	21-Apr-26 A	21-Apr-26 A	0.00	0.00	0.00	100%	100%	ROAD STAND	
DAM3-E-SS-R-870	ROAD STANDARD DETAILS-ROAD MARKING DETAILS	2	03-Mar-26	04-Mar-26	21-Apr-26 A	21-Apr-26 A	0.00	0.00	0.00	100%	100%	ROAD STAND	
DAM3-E-SS-R-790	ALIGNMENT & CURB SETTING OUT	2	10-Feb-26	11-Feb-26	14-Jun-26 A	14-Jun-26 A	0.00	0.00	0.00	100%	100%	ALIGNMENT	
DAM3-E-SS-R-800	ALIGNMENT & CURB SETTING OUT TABLES	2	12-Feb-26	14-Feb-26	14-Jun-26 A	14-Jun-26 A	0.00	0.00	0.00	100%	100%	ALIGNMENT	
DAM3-E-SS-R-810	ALIGNMNET GEOMETRIC DATA	2	15-Feb-26	16-Feb-26	14-Jun-26 A	14-Jun-26 A	0.00	0.00	0.00	100%	100%	ALIGNMNET	
DAM3-E-SS-R-820	SWEPT PATH LAYOUT PLAN	2	17-Feb-26	19-Feb-26	14-Jun-26 A	14-Jun-26 A	0.00	0.00	0.00	100%	100%	SWEPT PAT	
DAM3-E-SS-R-950	LANDSCAPE DETAILS	1	25-Mar-26	26-Mar-26	01-Jul-26 A	01-Jul-26 A	0.00	0.00	0.00	100%	100%	LANDSCAP	
EXTERNAL		74	01-Mar-26	07-May-26	10-Feb-26 A	02-Jun-26 A	0.00	0.00	0.00	0%	0%	02-Jun-26 A,	
DAM3-E-SS-EX-730	PIPE TRENCH DETAILS	2	10-Mar-26	11-Mar-26	10-Feb-26 A	10-Feb-26 A	0.00	0.00	0.00	100%	100%	PIPE TRENCH I	
DAM3-E-SS-EX-740	BURIED GATE VALVE DETAILS	2	12-Mar-26	14-Mar-26	10-Feb-26 A	10-Feb-26 A	0.00	0.00	0.00	100%	100%	BURIED GATE V	
DAM3-E-SS-EX-770	WASHOUT CHAMBER DETAILS	2	23-Mar-26	24-Mar-26	10-Feb-26 A	10-Feb-26 A	0.00	0.00	0.00	100%	100%	WASHOUT CHA	
DAM3-E-SS-EX-780	AIR RELEASE VALVE CHAMBER DETAILS	2	25-Mar-26	26-Mar-26	10-Feb-26 A	10-Feb-26 A	0.00	0.00	0.00	100%	100%	AIR RELEASE V	
DAM3-E-SS-EX-810	THRUST BLOCK DETAILS (SHEET 1 OF 4)	2	01-Apr-26	02-Apr-26	10-Feb-26 A	10-Feb-26 A	0.00	0.00	0.00	100%	100%	THRUST BLOCK	
DAM3-E-SS-EX-820	THRUST BLOCK DETAILS (SHEET 2 OF 4)	2	01-Apr-26	02-Apr-26	10-Feb-26 A	10-Feb-26 A	0.00	0.00	0.00	100%	100%	THRUST BLOCK	
DAM3-E-SS-EX-830	THRUST BLOCK DETAILS (SHEET 3 OF 4)	2	01-Apr-26	02-Apr-26	10-Feb-26 A	10-Feb-26 A	0.00	0.00	0.00	100%	100%	THRUST BLOCK	
DAM3-E-SS-EX-840	THRUST BLOCK DETAILS (SHEET 4 OF 4)	2	01-Apr-26	02-Apr-26	10-Feb-26 A	10-Feb-26 A	0.00	0.00	0.00	100%	100%	THRUST BLOCK	
DAM3-E-SS-EX-870	GENERAL NOTES	2	08-Apr-26	09-Apr-26	10-Feb-26 A	10-Feb-26 A	0.00	0.00	0.00	100%	100%	GENERAL NOTE	
DAM3-E-SS-EX-880	PIPE TRENCHES DETAILS (1)	2	11-Apr-26	12-Apr-26	10-Feb-26 A	10-Feb-26 A	0.00	0.00	0.00	100%	100%	PIPE TRENCHE	
DAM3-E-SS-EX-890	PIPE TRENCHES DETAILS (2)	2	13-Apr-26	14-Apr-26	10-Feb-26 A	10-Feb-26 A	0.00	0.00	0.00	100%	100%	PIPE TRENCHE	
DAM3-E-SS-EX-900	CAST IN PLACE MANHOLE DETAILS FOR DEPTH < 6000MM (TYPE-A)	2	15-Apr-26	16-Apr-26	10-Feb-26 A	10-Feb-26 A	0.00	0.00	0.00	100%	100%	CAST IN PLACE	
DAM3-E-SS-EX-920	BACKDROP DETAIL OF PRECAST MANHOLE DEPTH < 3000MM	2	15-Apr-26	16-Apr-26	10-Feb-26 A	10-Feb-26 A	0.00	0.00	0.00	100%	100%	BACKDROP DE	
DAM3-E-SS-EX-930	BACKDROP DETAIL OF PRECAST MANHOLE DEPTH FROM 3000MM TO	2	15-Apr-26	16-Apr-26	10-Feb-26 A	10-Feb-26 A	0.00	0.00	0.00	100%	100%	BACKDROP DE	
DAM3-E-SS-EX-960	PIPE TRENCH DETAILS	2	22-Apr-26	23-Apr-26	10-Feb-26 A	10-Feb-26 A	0.00	0.00	0.00	100%	100%	PIPE TRENCH I	
DAM3-E-SS-EX-970	BURIED GATE VALVE DETAILS	2	25-Apr-26	26-Apr-26	10-Feb-26 A	10-Feb-26 A	0.00	0.00	0.00	100%	100%	BURIED GATE V	
DAM3-E-SS-EX-1000	WASHOUT CHAMBER DETAILS	2	02-May-26	03-May-26	10-Feb-26 A	10-Feb-26 A	0.00	0.00	0.00	100%	100%	WASHOUT CHA	
DAM3-E-SS-EX-1010	AIR RELEASE VALVE CHAMBER DETAILS	2	04-May-26	05-May-26	10-Feb-26 A	10-Feb-26 A	0.00	0.00	0.00	100%	100%	AIR RELEASE V	
DAM3-E-SS-EX-1020	THRUST BLOCK DETAILS (SHEET 1 OF 4)	2	06-May-26	07-May-26	10-Feb-26 A	10-Feb-26 A	0.00	0.00	0.00	100%	100%	THRUST BLOCK	
DAM3-E-SS-EX-1030	THRUST BLOCK DETAILS (SHEET 2 OF 4)	2	06-May-26	07-May-26	10-Feb-26 A	10-Feb-26 A	0.00	0.00	0.00	100%	100%	THRUST BLOCK	
DAM3-E-SS-EX-1040	THRUST BLOCK DETAILS (SHEET 3 OF 4)	2	06-May-26	07-May-26	10-Feb-26 A	10-Feb-26 A	0.00	0.00	0.00	100%	100%	THRUST BLOCK	
DAM3-E-SS-EX-1050	THRUST BLOCK DETAILS (SHEET 4 OF 4)	2	06-May-26	07-May-26	10-Feb-26 A	10-Feb-26 A	0.00	0.00	0.00	100%	100%	THRUST BLOCK	
DAM3-E-SS-EX-910	CAST IN PLACE MANHOLE DETAILS FOR DEPTH < 6000MM (TYPE-B)	2	15-Apr-26	16-Apr-26	12-Feb-26 A	12-Feb-26 A	0.00	0.00	0.00	100%	100%	CAST IN PLACE	
DAM3-E-SS-EX-940	PRECAST MANHOLE DETAILS	2	18-Apr-26	19-Apr-26	15-Apr-26 A	15-Apr-26 A	0.00	0.00	0.00	100%	100%	PRECAST MA	
DAM3-E-SS-EX-750	SINGLE VALVE CHAMBER DETAILS	2	15-Mar-26	16-Mar-26	21-Apr-26 A	21-Apr-26 A	0.00	0.00	0.00	100%	100%	SINGLE VALV	
DAM3-E-SS-EX-760	DOUBLE VALVE CHAMBER DETAILS	2	21-Mar-26	22-Mar-26	21-Apr-26 A	21-Apr-26 A	0.00	0.00	0.00	100%	100%	DOUBLE VALV	
DAM3-E-SS-EX-980	SINGLE VALVE CHAMBER DETAILS	2	27-Apr-26	28-Apr-26	21-Apr-26 A	21-Apr-26 A	0.00	0.00	0.00	100%	100%	SINGLE VALV	
DAM3-E-SS-EX-990	DOUBLE VALVE CHAMBER DETAILS	2	29-Apr-26	30-Apr-26	21-Apr-26 A	21-Apr-26 A	0.00	0.00	0.00	100%	100%	DOUBLE VALV	
DAM3-E-SS-EX-690	POTABLE WATER NETWORK	2	01-Mar-26	02-Mar-26	11-May-26 A	11-May-26 A	0.00	0.00	0.00	100%	100%	POTABLE WA	
DAM3-E-SS-EX-700	FIRE FIGHTING WATER NETWORK	2	03-Mar-26	04-Mar-26	11-May-26 A	11-May-26 A	0.00	0.00	0.00	100%	100%	FIRE FIGHTIN	
DAM3-E-SS-EX-710	POTABLE WATER NETWORK PROFILES	2	05-Mar-26	07-Mar-26	11-May-26 A	11-May-26 A	0.00	0.00	0.00	100%	100%	POTABLE WA	
DAM3-E-SS-EX-720	FIRE FIGHTING NETWORK PROFILE	2	08-Mar-26	09-Mar-26	11-May-26 A	11-May-26 A	0.00	0.00	0.00	100%	100%	FIRE FIGHTIN	
DAM3-E-SS-EX-950	IRRIGATION NETWORK LAYOUT SHEET 1 OF 1	2	20-Apr-26	21-Apr-26	12-May-26 A	12-May-26 A	0.00	0.00	0.00	100%	100%	IRRIGATION	

Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary

Date	Revision	Checked	Approved
06-Oct-26	Weekly Report		

Activity ID	Activity Name	Original Duration	BL Project Start	BL Project Finish	Start	Finish	Budgeted Total Cost	Planned Value Cost	Earned Value Cost	Schedule % Complete	Performance % Complete	2026	2027
DAM3-E-SS-EX-850	SEWAGE NETWORK	2	04-Apr-26	05-Apr-26	14-May-26 A	14-May-26 A	0.00	0.00	0.00	100%	100%	SEWAGE NE	
DAM3-E-SS-EX-860	SEWAGE NETWORK PROFILES	2	06-Apr-26	07-Apr-26	14-May-26 A	14-May-26 A	0.00	0.00	0.00	100%	100%	SEWAGE NE	
DAM3-E-SS-EX-790	FLOW METER DETAILS	2	28-Mar-26	29-Mar-26	02-Jun-26 A	02-Jun-26 A	0.00	0.00	0.00	100%	100%	FLOW METE	
DAM3-E-SS-EX-800	FLOW METER REINFORCEMENT DETAILS	2	30-Mar-26	31-Mar-26	02-Jun-26 A	02-Jun-26 A	0.00	0.00	0.00	100%	100%	FLOW METE	
REVIEW AND APPROVAL		117	29-Jan-26	17-May-26	20-Jan-26 A	05-Jul-26 A	0.00	0.00	0.00	0%	0%	05-Jul-26 A,	
STRUCTURAL		87	12-Feb-26	24-Mar-26	03-Feb-26 A	03-Jun-26 A	0.00	0.00	0.00	0%	0%	03-Jun-26 A,	
DAM3-E-SA-C-830	SECTIONS	2	05-Mar-26	07-Mar-26	03-Feb-26 A	05-Feb-26 A	0.00	0.00	0.00	100%	100%	SECTIONS	
DAM3-E-SA-C-840	EXTERNAL WALL SECTION DETAILS	2	08-Mar-26	09-Mar-26	03-Feb-26 A	05-Feb-26 A	0.00	0.00	0.00	100%	100%	EXTERNAL WAL	
DAM3-E-SA-C-850	BASE PLATE DETAILS	2	10-Mar-26	11-Mar-26	03-Feb-26 A	05-Feb-26 A	0.00	0.00	0.00	100%	100%	BASE PLATE DE	
DAM3-E-SA-C-770	BASE PLATE LAYOUT	2	17-Feb-26	19-Feb-26	07-Feb-26 A	17-Mar-26 A	0.00	0.00	0.00	100%	100%	BASE PLATE L	
DAM3-E-SA-C-790	ROOF FRAMING LAYOUT	2	23-Feb-26	25-Feb-26	07-Feb-26 A	17-Mar-26 A	0.00	0.00	0.00	100%	100%	ROOF FRAMIN	
DAM3-E-SA-C-800	PURLINS FRAMING LAYOUT	2	25-Feb-26	28-Feb-26	07-Feb-26 A	17-Mar-26 A	0.00	0.00	0.00	100%	100%	PURLINS FRA	
DAM3-E-SA-C-810	ROOF SHEETING LAYOUT	2	01-Mar-26	02-Mar-26	07-Feb-26 A	17-Mar-26 A	0.00	0.00	0.00	100%	100%	ROOF SHEETI	
DAM3-E-SA-C-820	COLUMNS AND AXIS LAYOUT	2	03-Mar-26	04-Mar-26	07-Feb-26 A	07-Mar-26 A	0.00	0.00	0.00	100%	100%	COLUMNS AND	
DAM3-E-SA-C-750	FOUNDATION LAYOUT	2	12-Feb-26	14-Feb-26	18-Feb-26 A	07-Mar-26 A	0.00	0.00	0.00	100%	100%	FOUNDATION L	
DAM3-E-SA-C-780	TIE BEAM @ 4500mm EL.	2	19-Feb-26	23-Feb-26	01-Mar-26 A	17-May-26 A	0.00	0.00	0.00	100%	100%	TIE BEAM @	
DAM3-E-SA-C-880	PUMP SHED AND GRP WATER TANK STRUCTURAL DETAILS (1-2)	2	21-Mar-26	22-Mar-26	29-Mar-26 A	17-May-26 A	0.00	0.00	0.00	100%	100%	PUMP SHED	
DAM3-E-SA-C-890	PUMP SHED AND GRP WATER TANK STRUCTURAL DETAILS (2-2)	2	23-Mar-26	24-Mar-26	29-Mar-26 A	17-May-26 A	0.00	0.00	0.00	100%	100%	PUMP SHED	
DAM3-E-SA-C-760	GRADE BEAM / SLAB ON GRADE LAYOUT	2	15-Feb-26	16-Feb-26	21-Apr-26 A	03-May-26 A	0.00	0.00	0.00	100%	100%	GRADE BEAM	
DAM3-E-SA-C-860	TYPICAL STRUCTURAL SECTION DETAILS	2	12-Mar-26	14-Mar-26	21-Apr-26 A	12-May-26 A	0.00	0.00	0.00	100%	100%	TYPICAL STR	
DAM3-E-SA-C-870	STRUCTURAL SCHEDULE	2	15-Mar-26	16-Mar-26	02-Jun-26 A	03-Jun-26 A	0.00	0.00	0.00	100%	100%	STRUCTURA	
ARCHITECTURAL		75	01-Mar-26	06-Apr-26	03-Feb-26 A	03-Jun-26 A	0.00	0.00	0.00	0%	0%	03-Jun-26 A,	
DAM3-E-SA-A-830	GROUND FLOOR LAYOUT PLAN	2	01-Mar-26	02-Mar-26	03-Feb-26 A	08-Feb-26 A	0.00	0.00	0.00	100%	100%	GROUND FLOO	
DAM3-E-SA-A-840	GROUND FLOOR ENLARGED LAYOUT PLAN	2	03-Mar-26	04-Mar-26	03-Feb-26 A	08-Feb-26 A	0.00	0.00	0.00	100%	100%	GROUND FLOO	
DAM3-E-SA-A-860	ELEVATIONS (SHEET 01 0F 02)	2	08-Mar-26	09-Mar-26	03-Feb-26 A	05-Feb-26 A	0.00	0.00	0.00	100%	100%	ELEVATIONS (S	
DAM3-E-SA-A-870	ELEVATIONS (SHEET 01 0F 02)	2	10-Mar-26	11-Mar-26	03-Feb-26 A	05-Feb-26 A	0.00	0.00	0.00	100%	100%	ELEVATIONS (S	
DAM3-E-SA-A-880	WALL SECTIONS	2	14-Mar-26	15-Mar-26	03-Feb-26 A	05-Feb-26 A	0.00	0.00	0.00	100%	100%	WALL SECTION	
DAM3-E-SA-A-1170	BUILDING SECTIONS	5	12-Mar-26	21-Mar-26	03-Feb-26 A	05-Feb-26 A	0.00	0.00	0.00	100%	100%	BUILDING SECT	
DAM3-E-SA-A-890	CEILING LAYOUT PLAN	2	16-Mar-26	21-Mar-26	05-Feb-26 A	09-Feb-26 A	0.00	0.00	0.00	100%	100%	CEILING LAYOU	
DAM3-E-SA-A-900	FINISHING LAYOUT PLAN	2	22-Mar-26	23-Mar-26	09-Feb-26 A	14-Feb-26 A	0.00	0.00	0.00	100%	100%	FINISHING LAY	
DAM3-E-SA-A-910	TOILET DETAILS	2	24-Mar-26	25-Mar-26	11-Feb-26 A	25-Feb-26 A	0.00	0.00	0.00	100%	100%	TOILET DETAIL	
DAM3-E-SA-A-920	DOORS & WINDOWS SCHEDULE	2	26-Mar-26	28-Mar-26	11-Feb-26 A	25-Feb-26 A	0.00	0.00	0.00	100%	100%	DOORS & WIN	
DAM3-E-SA-A-930	MISCELLANEOUS DETAILS - 01	2	29-Mar-26	30-Mar-26	11-Feb-26 A	25-Feb-26 A	0.00	0.00	0.00	100%	100%	MISCELLANEO	
DAM3-E-SA-A-940	MISCELLANEOUS DETAILS - 02	2	31-Mar-26	01-Apr-26	11-Feb-26 A	25-Feb-26 A	0.00	0.00	0.00	100%	100%	MISCELLANEO	
DAM3-E-SA-A-950	SIGNAGE LOCATION PLAN	2	02-Apr-26	04-Apr-26	11-Feb-26 A	25-Feb-26 A	0.00	0.00	0.00	100%	100%	SIGNAGE LOCA	
DAM3-E-SA-A-960	SIGNAGE DESIGN DETAILS	2	05-Apr-26	06-Apr-26	11-Feb-26 A	25-Feb-26 A	0.00	0.00	0.00	100%	100%	SIGNAGE DESI	
DAM3-E-SA-A-850	SKYLIGHT DISTRIBUTION - ROOF LAYOUT PLAN	2	05-Mar-26	07-Mar-26	02-Jun-26 A	03-Jun-26 A	0.00	0.00	0.00	100%	100%	SKYLIGHT D	
MECHANICAL		51	05-Mar-26	26-Apr-26	04-Feb-26 A	09-Jun-26 A	0.00	0.00	0.00	0%	0%	09-Jun-26 A,	
DAM3-E-SA-M-650	SCHEMATIC RISER DIAGRAM PLUMBING-DRAINAGE	2	21-Mar-26	22-Mar-26	04-Feb-26 A	03-Mar-26 A	0.00	0.00	0.00	100%	100%	SCHEMATIC R	
DAM3-E-SA-M-660	SCHEMATIC RISER DIAGRAM PLUMBING-WATER	2	23-Mar-26	24-Mar-26	04-Feb-26 A	13-Apr-26 A	0.00	0.00	0.00	100%	100%	SCHEMATIC R	
DAM3-E-SA-M-670	GENERAL MISELLANEOUS DETAILS PLUMBING	2	25-Mar-26	26-Mar-26	04-Feb-26 A	03-Mar-26 A	0.00	0.00	0.00	100%	100%	GENERAL MIS	
DAM3-E-SA-M-680	GENERAL MISELLANEOUS DETAILS PLUMBING	2	28-Mar-26	29-Mar-26	04-Feb-26 A	03-Mar-26 A	0.00	0.00	0.00	100%	100%	GENERAL MIS	
DAM3-E-SA-M-750	GENERAL-INSTRUMENTATION & CONTROL	2	13-Apr-26	14-Apr-26	04-Feb-26 A	09-Jun-26 A	0.00	0.00	0.00	100%	100%	GENERAL-IN	
DAM3-E-SA-M-780	SCHEMATIC RISER DIAGRAM FIREFIGHTING	2	20-Apr-26	21-Apr-26	04-Feb-26 A	09-Jun-26 A	0.00	0.00	0.00	100%	100%	SCHEMATIC	
DAM3-E-SA-M-790	GENERAL-MISCELLANEOUS DETAILS- FIRE FIGHTING	2	22-Apr-26	23-Apr-26	04-Feb-26 A	09-Jun-26 A	0.00	0.00	0.00	100%	100%	GENERAL-M	
DAM3-E-SA-M-800	MISCELLANEOUS DETAILS	2	25-Apr-26	26-Apr-26	04-Feb-26 A	03-Mar-26 A	0.00	0.00	0.00	100%	100%	MISCELLANEO	
DAM3-E-SA-M-760	GENERAL MISCELLANEOUS DETAILS - HVAC	2	15-Apr-26	16-Apr-26	05-Feb-26 A	03-Mar-26 A	0.00	0.00	0.00	100%	100%	GENERAL MIS	
DAM3-E-SA-M-610	TOILETS DETAILS PLUMBING-DRAINAGE	2	08-Mar-26	09-Mar-26	11-Mar-26 A	10-May-26 A	0.00	0.00	0.00	100%	100%	TOILETS DET	
DAM3-E-SA-M-640	TOILET DETAILS PLUMBING-WATER	2	15-Mar-26	16-Mar-26	11-Mar-26 A	10-May-26 A	0.00	0.00	0.00	100%	100%	TOILET DETA	

Activity ID	Activity Name	Original Duration	BL Project Start	BL Project Finish	Start	Finish	Budgeted Total Cost	Planned Value Cost	Earned Value Cost	Schedule % Complete	Performance % Complete	2026 2027
DAM3-E-SA-M-770	TYPICAL GROUND FLOOR PLAN FIREFIGHTING	2	18-Apr-26	19-Apr-26	14-Mar-26 A	12-May-26 A	0.00	0.00	0.00	100%	100%	TYPICAL GR
DAM3-E-SA-M-620	TYPICAL ROOF PLUMBING PLAN	2	10-Mar-26	11-Mar-26	16-Mar-26 A	12-May-26 A	0.00	0.00	0.00	100%	100%	TYPICAL RO
DAM3-E-SA-M-600	TYPICAL GROUND FLOOR PLAN-PLUMBING- DRAINAGE	2	05-Mar-26	07-Mar-26	17-Mar-26 A	12-May-26 A	0.00	0.00	0.00	100%	100%	TYPICAL GR
DAM3-E-SA-M-630	GROUND FLOOR WATER SUPPLY PLAN	2	12-Mar-26	14-Mar-26	17-Mar-26 A	12-May-26 A	0.00	0.00	0.00	100%	100%	GROUND FL
DAM3-E-SA-M-690	SCHEDULE- PLUMBING	2	30-Mar-26	31-Mar-26	17-Mar-26 A	11-May-26 A	0.00	0.00	0.00	100%	100%	SCHEDULE-
DAM3-E-SA-M-720	SCHEDULES	2	06-Apr-26	07-Apr-26	17-Mar-26 A	11-May-26 A	0.00	0.00	0.00	100%	100%	SCHEDULES
DAM3-E-SA-M-730	GROUND FLOOR PLAN-HVAC SYSTEM	2	08-Apr-26	09-Apr-26	26-Mar-26 A	12-May-26 A	0.00	0.00	0.00	100%	100%	GROUND FL
DAM3-E-SA-M-740	TYPICAL ROOF HVAC PLAN	2	11-Apr-26	12-Apr-26	26-Mar-26 A	12-May-26 A	0.00	0.00	0.00	100%	100%	TYPICAL RO
DAM3-E-SA-M-700	PUMP ROOM LAYOUT	2	01-Apr-26	02-Apr-26	16-Apr-26 A	17-May-26 A	0.00	0.00	0.00	100%	100%	PUMP ROOM
DAM3-E-SA-M-710	PUMP ROOM 3D & SECTIONS VIEW	2	04-Apr-26	05-Apr-26	21-Apr-26 A	17-May-26 A	0.00	0.00	0.00	100%	100%	PUMP ROOM
ELECTRICAL		99	08-Mar-26	07-May-26	09-Feb-26 A	28-Jun-26 A	0.00	0.00	0.00	0%	0%	28-Jun-26 A
DAM3-E-SA-E-940	GROUND FLOOR POWER PLAN	2	08-Mar-26	09-Mar-26	09-Feb-26 A	10-Feb-26 A	0.00	0.00	0.00	100%	100%	GROUND FLOO
DAM3-E-SA-E-950	GROUND FLOOR POWER FOR MECHANICAL	2	10-Mar-26	11-Mar-26	09-Feb-26 A	18-Apr-26 A	0.00	0.00	0.00	100%	100%	GROUND FLO
DAM3-E-SA-E-960	ROOF FLOOR POWER FOR MECHANICAL	2	12-Mar-26	14-Mar-26	09-Feb-26 A	15-Apr-26 A	0.00	0.00	0.00	100%	100%	ROOF FLOOR
DAM3-E-SA-E-990	GROUND FLOOR LIGHTING PLAN	2	23-Mar-26	24-Mar-26	09-Feb-26 A	17-Feb-26 A	0.00	0.00	0.00	100%	100%	GROUND FLOO
DAM3-E-SA-E-1000	ROOF FLOOR LIGHTING PLAN	2	25-Mar-26	26-Mar-26	09-Feb-26 A	17-Feb-26 A	0.00	0.00	0.00	100%	100%	ROOF FLOOR L
DAM3-E-SA-E-1060	ROOF FLOOR LIGHTENING PLAN	2	08-Apr-26	09-Apr-26	09-Feb-26 A	17-Feb-26 A	0.00	0.00	0.00	100%	100%	ROOF FLOOR L
DAM3-E-SA-E-1130	GROUND FLOOR POWER PLAN	2	25-Apr-26	26-Apr-26	09-Feb-26 A	17-Feb-26 A	0.00	0.00	0.00	100%	100%	GROUND FLOO
DAM3-E-SA-E-1140	POWER FOR MECHANICAL	2	27-Apr-26	28-Apr-26	09-Feb-26 A	18-Feb-26 A	0.00	0.00	0.00	100%	100%	POWER FOR M
DAM3-E-SA-E-1150	GROUND FLOOR LIGHTING PLAN	2	29-Apr-26	30-Apr-26	09-Feb-26 A	17-Feb-26 A	0.00	0.00	0.00	100%	100%	GROUND FLOO
DAM3-E-SA-E-1030	GROUND FLOOR CCTV PLAN	2	01-Apr-26	02-Apr-26	01-Mar-26 A	03-Mar-26 A	0.00	0.00	0.00	100%	100%	GROUND FLOO
DAM3-E-SA-E-1040	GROUND FLOOR DATA & TELECOM PLAN	2	04-Apr-26	05-Apr-26	01-Mar-26 A	03-Mar-26 A	0.00	0.00	0.00	100%	100%	GROUND FLOO
DAM3-E-SA-E-1050	GROUND FLOOR GROUNDING PLAN	2	06-Apr-26	07-Apr-26	01-Mar-26 A	03-Mar-26 A	0.00	0.00	0.00	100%	100%	GROUND FLOO
DAM3-E-SA-E-1120	ELECTRICAL DETAILS	2	22-Apr-26	23-Apr-26	01-Mar-26 A	03-Mar-26 A	0.00	0.00	0.00	100%	100%	ELECTRICAL D
DAM3-E-SA-E-1160	GROUND FLOOR GROUNDING PLAN	2	02-May-26	03-May-26	01-Mar-26 A	03-Mar-26 A	0.00	0.00	0.00	100%	100%	GROUND FLOO
DAM3-E-SA-E-1180	ELECTRICAL DETAILS	2	06-May-26	07-May-26	01-Mar-26 A	03-Mar-26 A	0.00	0.00	0.00	100%	100%	ELECTRICAL D
DAM3-E-SA-E-1010	GOUND FLOOR ACCESS CONTROL	2	28-Mar-26	29-Mar-26	29-Mar-26 A	18-Apr-26 A	0.00	0.00	0.00	100%	100%	GOUND FLOO
DAM3-E-SA-E-1020	GROUND FLOOR FIRE ALARM PLAN	2	30-Mar-26	31-Mar-26	29-Mar-26 A	15-Apr-26 A	0.00	0.00	0.00	100%	100%	GROUND FLO
DAM3-E-SA-E-1070	POWER RISER DIAGRAM	2	11-Apr-26	12-Apr-26	29-Mar-26 A	23-Jun-26 A	0.00	0.00	0.00	100%	100%	POWER RIS
DAM3-E-SA-E-1080	FIRE ALARM RISER DIAGRAM	2	13-Apr-26	14-Apr-26	29-Mar-26 A	11-May-26 A	0.00	0.00	0.00	100%	100%	FIRE ALARM
DAM3-E-SA-E-1090	DATA & TELECOME RISER DIAGRAM	2	15-Apr-26	16-Apr-26	29-Mar-26 A	30-Mar-26 A	0.00	0.00	0.00	100%	100%	DATA & TELEC
DAM3-E-SA-E-1100	ACCESS CONTROL RISER DIAGRAM	2	18-Apr-26	19-Apr-26	29-Mar-26 A	30-Mar-26 A	0.00	0.00	0.00	100%	100%	ACCESS CON
DAM3-E-SA-E-1110	SCHEDULES	2	20-Apr-26	21-Apr-26	29-Mar-26 A	23-Jun-26 A	0.00	0.00	0.00	100%	100%	SCHEDULE
DAM3-E-SA-E-970	ROOF FLOOR POWER	2	15-Mar-26	16-Mar-26	08-Apr-26 A	09-Apr-26 A	0.00	0.00	0.00	100%	100%	ROOF FLOOR
DAM3-E-SA-E-1170	RISER DIAGRAM	2	04-May-26	05-May-26	27-Apr-26 A	23-Jun-26 A	0.00	0.00	0.00	100%	100%	RISER DIAG
DAM3-E-SA-E-980	PV SYSTEM CALCULATION	2	21-Mar-26	22-Mar-26	25-Jun-26 A	28-Jun-26 A	0.00	0.00	0.00	100%	100%	PV SYSTEM
ROAD DRAWINGS		117	29-Jan-26	31-Mar-26	20-Jan-26 A	05-Jul-26 A	0.00	0.00	0.00	0%	0%	05-Jul-26 A,
DAM3-E-SA-R-780	TOPOGRAPHIC SURVEY-CONTOURS MAP	2	10-Feb-26	11-Feb-26	20-Jan-26 A	22-Jan-26 A	0.00	0.00	0.00	100%	100%	TOPOGRAPHIC
DAM3-E-SA-R-730	GRADING LAYOUT PLAN	2	29-Jan-26	31-Jan-26	03-Feb-26 A	03-May-26 A	0.00	0.00	0.00	100%	100%	GRADING LA
DAM3-E-SA-R-880	GENERAL SITE PLAN - OVERALL	2	08-Mar-26	09-Mar-26	08-Mar-26 A	20-May-26 A	0.00	0.00	0.00	100%	100%	GENERAL SI
DAM3-E-SA-R-890	SITE SETTING-OUT PLAN - OVERALL	2	10-Mar-26	11-Mar-26	08-Mar-26 A	03-May-26 A	0.00	0.00	0.00	100%	100%	SITE SETTIN
DAM3-E-SA-R-900	GENERAL LANDSCAPE LAYOUT	2	12-Mar-26	14-Mar-26	08-Mar-26 A	06-May-26 A	0.00	0.00	0.00	100%	100%	GENERAL LA
DAM3-E-SA-R-910	GENERAL HARDSCAPE LAYOUT	2	15-Mar-26	16-Mar-26	08-Mar-26 A	07-May-26 A	0.00	0.00	0.00	100%	100%	GENERAL HA
DAM3-E-SA-R-920	GENERAL SOFTSCAPE LAYOUT	2	21-Mar-26	22-Mar-26	08-Mar-26 A	09-May-26 A	0.00	0.00	0.00	100%	100%	GENERAL SC
DAM3-E-SA-R-960	LANDSCAPE SCHEDULES	2	30-Mar-26	31-Mar-26	08-Mar-26 A	06-May-26 A	0.00	0.00	0.00	100%	100%	LANDSCAPE
DAM3-E-SA-R-930	PUMP ROOM DETAILS	2	23-Mar-26	24-Mar-26	14-Mar-26 A	06-May-26 A	0.00	0.00	0.00	100%	100%	PUMP ROOM
DAM3-E-SA-R-740	ROAD LAYOUT PLAN	2	01-Feb-26	02-Feb-26	16-Mar-26 A	29-Apr-26 A	0.00	0.00	0.00	100%	100%	ROAD LAYOU
DAM3-E-SA-R-750	TYPICAL CROSS SECTIONS - KEY PLAN	2	03-Feb-26	04-Feb-26	16-Mar-26 A	04-May-26 A	0.00	0.00	0.00	100%	100%	TYPICAL CRO
DAM3-E-SA-R-760	TYPICAL CROSS SECTIONS	2	05-Feb-26	07-Feb-26	16-Mar-26 A	04-May-26 A	0.00	0.00	0.00	100%	100%	TYPICAL CRO

Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary

Date	Revision	Checked	Approved
06-Oct-26	Weekly Report		


Activity ID	Activity Name	Original Duration	BL Project Start	BL Project Finish	Start	Finish	Budgeted Total Cost	Planned Value Cost	Earned Value Cost	Schedule % Complete	Performance % Complete	2026 2027
DAM3-E-SA-R-770	ROAD PROFILES	2	08-Feb-26	09-Feb-26	16-Mar-26 A	29-Apr-26 A	0.00	0.00	0.00	100%	100%	ROAD PROFI
DAM3-E-SA-R-940	GENERAL DETAILS	2	25-Mar-26	26-Mar-26	18-Mar-26 A	11-May-26 A	0.00	0.00	0.00	100%	100%	GENERAL DE
DAM3-E-SA-R-830	SIGNING & MARKING LAYOUT PLAN	2	23-Feb-26	25-Feb-26	21-Apr-26 A	29-Apr-26 A	0.00	0.00	0.00	100%	100%	SIGNING & M
DAM3-E-SA-R-840	ROAD STANDARD DETAILS-TYPICAL PAVEMENT DETAILS	2	25-Feb-26	28-Feb-26	21-Apr-26 A	04-May-26 A	0.00	0.00	0.00	100%	100%	ROAD STAND
DAM3-E-SA-R-850	ROAD STANDARD DETAILS-TYPICAL CURB DETAILS	2	01-Mar-26	02-Mar-26	21-Apr-26 A	04-May-26 A	0.00	0.00	0.00	100%	100%	ROAD STAND
DAM3-E-SA-R-860	ROAD STANDARD DETAILS-ROAD SIGN DETAILS	2	03-Mar-26	04-Mar-26	21-Apr-26 A	04-May-26 A	0.00	0.00	0.00	100%	100%	ROAD STAND
DAM3-E-SA-R-870	ROAD STANDARD DETAILS-ROAD MARKING DETAILS	2	05-Mar-26	07-Mar-26	21-Apr-26 A	04-May-26 A	0.00	0.00	0.00	100%	100%	ROAD STAND
DAM3-E-SA-R-790	ALIGNMENT & CURB SETTING OUT	2	12-Feb-26	14-Feb-26	14-Jun-26 A	14-Jun-26 A	0.00	0.00	0.00	100%	100%	ALIGNMENT
DAM3-E-SA-R-800	ALIGNMENT & CURB SETTING OUT TABLES	2	15-Feb-26	16-Feb-26	14-Jun-26 A	14-Jun-26 A	0.00	0.00	0.00	100%	100%	ALIGNMENT
DAM3-E-SA-R-810	ALIGNMNET GEOMETRIC DATA	2	17-Feb-26	19-Feb-26	14-Jun-26 A	14-Jun-26 A	0.00	0.00	0.00	100%	100%	ALIGNMNET
DAM3-E-SA-R-820	SWEPT PATH LAYOUT PLAN	2	19-Feb-26	23-Feb-26	14-Jun-26 A	14-Jun-26 A	0.00	0.00	0.00	100%	100%	SWEPT PAT
DAM3-E-SA-R-950	LANDSCAPE DETAILS	2	28-Mar-26	29-Mar-26	01-Jul-26 A	05-Jul-26 A	0.00	0.00	0.00	100%	100%	LANDSCAP
EXTERNAL		78	03-Mar-26	17-May-26	10-Feb-26 A	08-Jun-26 A	0.00	0.00	0.00	0%	0%	08-Jun-26 A,
DAM3-E-SA-EX-730	PIPE TRENCH DETAILS	2	12-Mar-26	14-Mar-26	10-Feb-26 A	10-May-26 A	0.00	0.00	0.00	100%	100%	PIPE TRENC
DAM3-E-SA-EX-740	BURIED GATE VALVE DETAILS	2	15-Mar-26	16-Mar-26	10-Feb-26 A	31-May-26 A	0.00	0.00	0.00	100%	100%	BURIED GAT
DAM3-E-SA-EX-770	WASHOUT CHAMBER DETAILS	2	25-Mar-26	26-Mar-26	10-Feb-26 A	11-May-26 A	0.00	0.00	0.00	100%	100%	WASHOUT C
DAM3-E-SA-EX-780	AIR RELEASE VALVE CHAMBER DETAILS	2	28-Mar-26	29-Mar-26	10-Feb-26 A	25-May-26 A	0.00	0.00	0.00	100%	100%	AIR RELEAS
DAM3-E-SA-EX-830	THRUST BLOCK DETAILS (SHEET 3 OF 4)	2	04-Apr-26	05-Apr-26	10-Feb-26 A	18-Mar-26 A	0.00	0.00	0.00	100%	100%	THRUST BLOC
DAM3-E-SA-EX-840	THRUST BLOCK DETAILS (SHEET 4 OF 4)	2	04-Apr-26	05-Apr-26	10-Feb-26 A	18-Mar-26 A	0.00	0.00	0.00	100%	100%	THRUST BLOC
DAM3-E-SA-EX-870	GENERAL NOTES	2	11-Apr-26	12-Apr-26	10-Feb-26 A	18-Mar-26 A	0.00	0.00	0.00	100%	100%	GENERAL NOT
DAM3-E-SA-EX-880	PIPE TRENCHES DETAILS (1)	2	13-Apr-26	14-Apr-26	10-Feb-26 A	18-Mar-26 A	0.00	0.00	0.00	100%	100%	PIPE TRENCH
DAM3-E-SA-EX-890	PIPE TRENCHES DETAILS (2)	2	15-Apr-26	16-Apr-26	10-Feb-26 A	18-Mar-26 A	0.00	0.00	0.00	100%	100%	PIPE TRENCH
DAM3-E-SA-EX-900	CAST IN PLACE MANHOLE DETAILS FOR DEPTH < 6000MM (TYPE-A)	2	18-Apr-26	19-Apr-26	10-Feb-26 A	11-May-26 A	0.00	0.00	0.00	100%	100%	CAST IN PLA
DAM3-E-SA-EX-920	BACKDROP DETAIL OF PRECAST MANHOLE DEPTH FROM 3000MM TO	2	18-Apr-26	19-Apr-26	10-Feb-26 A	19-May-26 A	0.00	0.00	0.00	100%	100%	BACKDROP
DAM3-E-SA-EX-930	BACKDROP DETAIL OF PRECAST MANHOLE DEPTH < 3000MM	2	18-Apr-26	19-Apr-26	10-Feb-26 A	19-May-26 A	0.00	0.00	0.00	100%	100%	BACKDROP
DAM3-E-SA-EX-960	PIPE TRENCH DETAILS	2	25-Apr-26	26-Apr-26	10-Feb-26 A	18-Mar-26 A	0.00	0.00	0.00	100%	100%	PIPE TRENCH
DAM3-E-SA-EX-970	BURIED GATE VALVE DETAILS	2	27-Apr-26	28-Apr-26	10-Feb-26 A	31-May-26 A	0.00	0.00	0.00	100%	100%	BURIED GAT
DAM3-E-SA-EX-1000	WASHOUT CHAMBER DETAILS	2	04-May-26	05-May-26	10-Feb-26 A	11-May-26 A	0.00	0.00	0.00	100%	100%	WASHOUT C
DAM3-E-SA-EX-1010	AIR RELEASE VALVE CHAMBER DETAILS	2	06-May-26	07-May-26	10-Feb-26 A	25-May-26 A	0.00	0.00	0.00	100%	100%	AIR RELEAS
DAM3-E-SA-EX-1020	THRUST BLOCK DETAILS (SHEET 1 OF 4)	2	09-May-26	10-May-26	10-Feb-26 A	18-Mar-26 A	0.00	0.00	0.00	100%	100%	THRUST BLOC
DAM3-E-SA-EX-1030	THRUST BLOCK DETAILS (SHEET 2 OF 4)	2	11-May-26	12-May-26	10-Feb-26 A	18-Mar-26 A	0.00	0.00	0.00	100%	100%	THRUST BLOC
DAM3-E-SA-EX-1040	THRUST BLOCK DETAILS (SHEET 3 OF 4)	2	13-May-26	14-May-26	10-Feb-26 A	18-Mar-26 A	0.00	0.00	0.00	100%	100%	THRUST BLOC
DAM3-E-SA-EX-1050	THRUST BLOCK DETAILS (SHEET 4 OF 4)	2	16-May-26	17-May-26	10-Feb-26 A	18-Mar-26 A	0.00	0.00	0.00	100%	100%	THRUST BLOC
DAM3-E-SA-EX-810	THRUST BLOCK DETAILS (SHEET 1 OF 4)	2	04-Apr-26	05-Apr-26	10-Feb-26 A	18-Mar-26 A	0.00	0.00	0.00	100%	100%	THRUST BLOC
DAM3-E-SA-EX-820	THRUST BLOCK DETAILS (SHEET 2 OF 4)	2	06-Apr-26	07-Apr-26	10-Feb-26 A	18-Mar-26 A	0.00	0.00	0.00	100%	100%	THRUST BLOC
DAM3-E-SA-EX-910	CAST IN PLACE MANHOLE DETAILS FOR DEPTH < 6000MM (TYPE-B)	2	18-Apr-26	19-Apr-26	12-Feb-26 A	11-May-26 A	0.00	0.00	0.00	100%	100%	CAST IN PLA
DAM3-E-SA-EX-940	PRECAST MANHOLE DETAILS	2	20-Apr-26	21-Apr-26	15-Apr-26 A	08-Jun-26 A	0.00	0.00	0.00	100%	100%	PRECAST M
DAM3-E-SA-EX-750	SINGLE VALVE CHAMBER DETAILS	2	21-Mar-26	22-Mar-26	21-Apr-26 A	27-Apr-26 A	0.00	0.00	0.00	100%	100%	SINGLE VALV
DAM3-E-SA-EX-760	DOUBLE VALVE CHAMBER DETAILS	2	23-Mar-26	24-Mar-26	21-Apr-26 A	27-Apr-26 A	0.00	0.00	0.00	100%	100%	DOUBLE VAL
DAM3-E-SA-EX-980	SINGLE VALVE CHAMBER DETAILS	2	29-Apr-26	30-Apr-26	21-Apr-26 A	27-Apr-26 A	0.00	0.00	0.00	100%	100%	SINGLE VALV
DAM3-E-SA-EX-990	DOUBLE VALVE CHAMBER DETAILS	2	02-May-26	03-May-26	21-Apr-26 A	27-Apr-26 A	0.00	0.00	0.00	100%	100%	DOUBLE VAL
DAM3-E-SA-EX-690	POTABLE WATER NETWORK	2	03-Mar-26	04-Mar-26	11-May-26 A	01-Jun-26 A	0.00	0.00	0.00	100%	100%	POTABLE W
DAM3-E-SA-EX-700	FIRE FIGHTING WATER NETWORK	2	05-Mar-26	07-Mar-26	11-May-26 A	12-May-26 A	0.00	0.00	0.00	100%	100%	FIRE FIGHTIN
DAM3-E-SA-EX-710	POTABLE WATER NETWORK PROFILES	2	08-Mar-26	09-Mar-26	11-May-26 A	25-May-26 A	0.00	0.00	0.00	100%	100%	POTABLE W
DAM3-E-SA-EX-720	FIRE FIGHTING NETWORK PROFILE	2	10-Mar-26	11-Mar-26	11-May-26 A	12-May-26 A	0.00	0.00	0.00	100%	100%	FIRE FIGHTIN
DAM3-E-SA-EX-950	IRRIGATION NETWORK LAYOUT SHEET 1 OF 1	2	22-Apr-26	23-Apr-26	12-May-26 A	17-May-26 A	0.00	0.00	0.00	100%	100%	IRRIGATION
DAM3-E-SA-EX-850	SEWAGE NETWORK	2	06-Apr-26	07-Apr-26	14-May-26 A	17-May-26 A	0.00	0.00	0.00	100%	100%	SEWAGE NE
DAM3-E-SA-EX-860	SEWAGE NETWORK PROFILES	2	08-Apr-26	09-Apr-26	14-May-26 A	17-May-26 A	0.00	0.00	0.00	100%	100%	SEWAGE NE
DAM3-E-SA-EX-790	FLOW METER DETAILS	2	30-Mar-26	31-Mar-26	02-Jun-26 A	03-Jun-26 A	0.00	0.00	0.00	100%	100%	FLOW METE

Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary

Date	Revision	Checked	Approved
06-Oct-26	Weekly Report		

Activity ID	Activity Name	Original Duration	BL Project Start	BL Project Finish	Start	Finish	Budgeted Total Cost	Planned Value Cost	Earned Value Cost	Schedule % Complete	Performance % Complete	2026 2027
DAM3-E-SA-EX-800	FLOW METER REINFORCEMENT DETAILS	2	01-Apr-26	02-Apr-26	02-Jun-26 A	03-Jun-26 A	0.00	0.00	0.00	100%	100%	FLOW METE
PRE QUALIFACTION FOR MATERIALS		138	22-Jan-26	12-Apr-26	15-Jan-26 A	11-Jun-26 A	0.00	0.00	0.00	0%	0%	11-Jun-26 A,
PREPARATION AND SUBMITTAL		108	22-Jan-26	09-Apr-26	15-Jan-26 A	10-Jun-26 A	0.00	0.00	0.00	0%	0%	10-Jun-26 A,
STRUCTURAL		10	22-Jan-26	02-Feb-26	15-Jan-26 A	19-Jan-26 A	0.00	0.00	0.00	0%	0%	19-Jan-26 A, STR
DAM3-E-PS-C-0010	Anti termite	2	22-Jan-26	24-Jan-26	15-Jan-26 A	15-Jan-26 A	0.00	0.00	0.00	100%	100%	Anti termite
DAM3-E-PS-C-0020	Concrete mix	2	25-Jan-26	26-Jan-26	15-Jan-26 A	15-Jan-26 A	0.00	0.00	0.00	100%	100%	Concrete mix
DAM3-E-PS-C-0040	Bitumen paint	2	29-Jan-26	31-Jan-26	15-Jan-26 A	15-Jan-26 A	0.00	0.00	0.00	100%	100%	Bitumen paint
DAM3-E-PS-C-0050	Rebar	2	01-Feb-26	02-Feb-26	15-Jan-26 A	15-Jan-26 A	0.00	0.00	0.00	100%	100%	Rebar
DAM3-E-PS-C-0030	Polyethylene sheet	2	27-Jan-26	28-Jan-26	19-Jan-26 A	19-Jan-26 A	0.00	0.00	0.00	100%	100%	Polyethylene she
ARCHITECTURAL		100	25-Jan-26	02-Mar-26	08-Feb-26 A	10-Jun-26 A	0.00	0.00	0.00	0%	0%	10-Jun-26 A,
DAM3-E-PS-A-0040	Concrete masonry unit (CMU)	2	27-Jan-26	28-Jan-26	08-Feb-26 A	08-Feb-26 A	0.00	0.00	0.00	100%	100%	Concrete mason
DAM3-E-PS-A-0130	Windows	2	08-Feb-26	09-Feb-26	08-Feb-26 A	08-Feb-26 A	0.00	0.00	0.00	100%	100%	Windows
DAM3-E-PS-A-0200	Aluminum Composite Panel	2	23-Feb-26	25-Feb-26	10-Feb-26 A	10-Feb-26 A	0.00	0.00	0.00	100%	100%	Aluminum Comp
DAM3-E-PS-A-0120	Doors	2	05-Feb-26	07-Feb-26	16-Feb-26 A	16-Feb-26 A	0.00	0.00	0.00	100%	100%	Doors
DAM3-E-PS-A-0020	PES -Steel Structure	2	25-Jan-26	26-Jan-26	19-Feb-26 A	23-Feb-26 A	0.00	0.00	0.00	100%	100%	PES -Steel Struc
DAM3-E-PS-A-0190	Gypsum board	2	19-Feb-26	23-Feb-26	24-Feb-26 A	24-Feb-26 A	0.00	0.00	0.00	100%	100%	Gypsum board
DAM3-E-PS-A-0050	Steel ladder	2	29-Jan-26	31-Jan-26	25-Feb-26 A	28-Feb-26 A	0.00	0.00	0.00	100%	100%	Steel ladder
DAM3-E-PS-A-0140	Ceramic tiles	2	10-Feb-26	11-Feb-26	25-Mar-26 A	25-Mar-26 A	0.00	0.00	0.00	100%	100%	Ceramic tiles
DAM3-E-PS-A-0180	Interni paint	2	17-Feb-26	19-Feb-26	25-Mar-26 A	25-Mar-26 A	0.00	0.00	0.00	100%	100%	Interni paint
DAM3-E-PS-A-0170	Epoxy paint	2	15-Feb-26	16-Feb-26	20-Apr-26 A	20-Apr-26 A	0.00	0.00	0.00	100%	100%	Epoxy paint
DAM3-E-PS-A-0150	Granite strip	2	12-Feb-26	14-Feb-26	03-May-26 A	03-May-26 A	0.00	0.00	0.00	100%	100%	Granite strip
DAM3-E-PS-A-0060	Steel gratings	2	01-Feb-26	02-Feb-26	19-May-26 A	19-May-26 A	0.00	0.00	0.00	100%	100%	Steel gratings
DAM3-E-PS-A-0230	Steel fence and gates	2	25-Feb-26	28-Feb-26	20-May-26 A	20-May-26 A	0.00	0.00	0.00	100%	100%	Steel fence a
DAM3-E-PS-A-0070	Steel rails	2	03-Feb-26	04-Feb-26	10-Jun-26 A	10-Jun-26 A	0.00	0.00	0.00	100%	100%	Steel rails
DAM3-E-PS-A-0240	Identification sign; ID01 & ID02	2	01-Mar-26	02-Mar-26	10-Jun-26 A	10-Jun-26 A	0.00	0.00	0.00	100%	100%	Identification
MECHANICAL		98	27-Jan-26	09-Apr-26	24-Jan-26 A	10-Jun-26 A	0.00	0.00	0.00	0%	0%	10-Jun-26 A,
DAM3-E-PS-M-0330	GRP tank	2	04-Apr-26	05-Apr-26	24-Jan-26 A	28-Jan-26 A	0.00	0.00	0.00	100%	100%	GRP tank
DAM3-E-PS-M-0250	Inline exhaust fans	2	23-Mar-26	24-Mar-26	02-Feb-26 A	02-Feb-26 A	0.00	0.00	0.00	100%	100%	Inline exhaust fa
DAM3-E-PS-M-0260	Wall propeller type exhaust fans	2	25-Mar-26	26-Mar-26	02-Feb-26 A	02-Feb-26 A	0.00	0.00	0.00	100%	100%	Wall propeller typ
DAM3-E-PS-M-0280	Fire fighting valves	2	30-Mar-26	31-Mar-26	02-Feb-26 A	02-Feb-26 A	0.00	0.00	0.00	100%	100%	Fire fighting valve
DAM3-E-PS-M-0340	Water supply valves	2	06-Apr-26	07-Apr-26	02-Feb-26 A	02-Feb-26 A	0.00	0.00	0.00	100%	100%	Water supply val
DAM3-E-PS-M-0030	PPR pipes	2	29-Jan-26	31-Jan-26	03-Feb-26 A	03-Feb-26 A	0.00	0.00	0.00	100%	100%	PPR pipes
DAM3-E-PS-M-0270	Fire pumps	2	28-Mar-26	29-Mar-26	03-Feb-26 A	03-Feb-26 A	0.00	0.00	0.00	100%	100%	Fire pumps
DAM3-E-PS-M-0320	Booster pump	2	01-Apr-26	02-Apr-26	03-Feb-26 A	03-Feb-26 A	0.00	0.00	0.00	100%	100%	Booster pump
DAM3-E-PS-M-0070	U/G HDPE pipes	2	08-Feb-26	09-Feb-26	04-Feb-26 A	04-Feb-26 A	0.00	0.00	0.00	100%	100%	U/G HDPE pipes
DAM3-E-PS-M-0090	Fire hose cabinet	2	10-Feb-26	11-Feb-26	04-Feb-26 A	04-Feb-26 A	0.00	0.00	0.00	100%	100%	Fire hose cabinet
DAM3-E-PS-M-0160	UPVC pipes	2	25-Feb-26	28-Feb-26	04-Feb-26 A	04-Feb-26 A	0.00	0.00	0.00	100%	100%	UPVC pipes
DAM3-E-PS-M-0200	Electric water heater	2	08-Mar-26	09-Mar-26	05-Feb-26 A	05-Feb-26 A	0.00	0.00	0.00	100%	100%	Electric water hea
DAM3-E-PS-M-0210	Western water closet	2	10-Mar-26	11-Mar-26	05-Feb-26 A	05-Feb-26 A	0.00	0.00	0.00	100%	100%	Western water cl
DAM3-E-PS-M-0240	Lavatory / wash basin	2	21-Mar-26	22-Mar-26	05-Feb-26 A	05-Feb-26 A	0.00	0.00	0.00	100%	100%	Lavatory / wash b
DAM3-E-PS-M-0190	Gully trap	2	05-Mar-26	07-Mar-26	07-Feb-26 A	07-Feb-26 A	0.00	0.00	0.00	100%	100%	Gully trap
DAM3-E-PS-M-0230	Toilet Fittings	2	15-Mar-26	16-Mar-26	07-Feb-26 A	07-Feb-26 A	0.00	0.00	0.00	100%	100%	Toilet Fittings
DAM3-E-PS-M-0010	Seamless black steel or ERW pipes	2	27-Jan-26	28-Jan-26	08-Feb-26 A	08-Feb-26 A	0.00	0.00	0.00	100%	100%	Seamless black s
DAM3-E-PS-M-0100	Automatic air release valve	2	12-Feb-26	14-Feb-26	08-Feb-26 A	08-Feb-26 A	0.00	0.00	0.00	100%	100%	Automatic air rele
DAM3-E-PS-M-0110	OS & Y gate valve	2	15-Feb-26	16-Feb-26	08-Feb-26 A	08-Feb-26 A	0.00	0.00	0.00	100%	100%	OS & Y gate valv
DAM3-E-PS-M-0120	Fire alarm check valve	2	17-Feb-26	19-Feb-26	08-Feb-26 A	08-Feb-26 A	0.00	0.00	0.00	100%	100%	Fire alarm check
DAM3-E-PS-M-0040	HVAC duct	2	01-Feb-26	02-Feb-26	09-Feb-26 A	09-Feb-26 A	0.00	0.00	0.00	100%	100%	HVAC duct
DAM3-E-PS-M-0050	Flexible duct	2	03-Feb-26	04-Feb-26	09-Feb-26 A	09-Feb-26 A	0.00	0.00	0.00	100%	100%	Flexible duct
DAM3-E-PS-M-0140	Ball valve	2	19-Feb-26	23-Feb-26	11-Feb-26 A	12-Feb-26 A	0.00	0.00	0.00	100%	100%	Ball valve


Activity ID	Activity Name	Original Duration	BL Project Start	BL Project Finish	Start	Finish	Budgeted Total Cost	Planned Value Cost	Earned Value Cost	Schedule % Complete	Performance % Complete
DAM3-E-PS-M-0350	Water tap	2	08-Apr-26	09-Apr-26	11-Feb-26 A	11-Feb-26 A	0.00	0.00	0.00	100%	100%
DAM3-E-PS-M-0080	Warning tapes	2	08-Feb-26	09-Feb-26	14-Feb-26 A	14-Feb-26 A	0.00	0.00	0.00	100%	100%
DAM3-E-PS-M-0170	Roof vent caps	2	01-Mar-26	02-Mar-26	16-Feb-26 A	16-Feb-26 A	0.00	0.00	0.00	100%	100%
DAM3-E-PS-M-0180	Floor drain	2	03-Mar-26	04-Mar-26	16-Feb-26 A	16-Feb-26 A	0.00	0.00	0.00	100%	100%
DAM3-E-PS-M-0220	Bib tap	2	12-Mar-26	14-Mar-26	04-Apr-26 A	05-Apr-26 A	0.00	0.00	0.00	100%	100%
DAM3-E-PS-M-0060	Exhaust diffuser	2	05-Feb-26	07-Feb-26	27-May-26 A	27-May-26 A	0.00	0.00	0.00	100%	100%
DAM3-E-PS-M-0150	Capped connection	2	23-Feb-26	25-Feb-26	10-Jun-26 A	10-Jun-26 A	0.00	0.00	0.00	100%	100%
ELECTRICAL		85	29-Jan-26	05-Apr-26	07-Feb-26 A	20-Apr-26 A	0.00	0.00	0.00	0%	0%
DAM3-E-PS-E-0010	PVC conduits	2	29-Jan-26	31-Jan-26	07-Feb-26 A	07-Feb-26 A	0.00	0.00	0.00	100%	100%
DAM3-E-PS-E-0180	Fire alarm system	2	12-Mar-26	14-Mar-26	09-Feb-26 A	09-Feb-26 A	0.00	0.00	0.00	100%	100%
DAM3-E-PS-E-0240	Access control system	2	28-Mar-26	29-Mar-26	09-Feb-26 A	09-Feb-26 A	0.00	0.00	0.00	100%	100%
DAM3-E-PS-E-0170	Wall mounted, duplex, telephone and data outlet	2	10-Mar-26	11-Mar-26	11-Feb-26 A	11-Feb-26 A	0.00	0.00	0.00	100%	100%
DAM3-E-PS-E-0230	CCTV System	2	25-Mar-26	26-Mar-26	11-Feb-26 A	11-Feb-26 A	0.00	0.00	0.00	100%	100%
DAM3-E-PS-E-0250	Solar system	2	30-Mar-26	31-Mar-26	24-Feb-26 A	01-Mar-26 A	0.00	0.00	0.00	100%	100%
DAM3-E-PS-E-0120	Suspended High Bay LED lights	2	25-Feb-26	28-Feb-26	01-Mar-26 A	01-Mar-26 A	0.00	0.00	0.00	100%	100%
DAM3-E-PS-E-0130	Flood lights	2	01-Mar-26	02-Mar-26	01-Mar-26 A	01-Mar-26 A	0.00	0.00	0.00	100%	100%
DAM3-E-PS-E-0140	Recessed mounted LED downlight	2	03-Mar-26	04-Mar-26	01-Mar-26 A	01-Mar-26 A	0.00	0.00	0.00	100%	100%
DAM3-E-PS-E-0150	LED Emergency Lights wall mounted	2	05-Mar-26	07-Mar-26	01-Mar-26 A	01-Mar-26 A	0.00	0.00	0.00	100%	100%
DAM3-E-PS-E-0160	LED Emergency Exit Light	2	08-Mar-26	09-Mar-26	01-Mar-26 A	01-Mar-26 A	0.00	0.00	0.00	100%	100%
DAM3-E-PS-E-0200	Street Lighting poles	1	15-Mar-26	16-Mar-26	01-Mar-26 A	01-Mar-26 A	0.00	0.00	0.00	100%	100%
DAM3-E-PS-E-0220	Surface mounted lights	2	23-Mar-26	24-Mar-26	01-Mar-26 A	01-Mar-26 A	0.00	0.00	0.00	100%	100%
DAM3-E-PS-E-0050	Wiring devices	2	08-Feb-26	09-Feb-26	03-Mar-26 A	03-Mar-26 A	0.00	0.00	0.00	100%	100%
DAM3-E-PS-E-0030	Cable Tray	2	03-Feb-26	04-Feb-26	03-Mar-26 A	03-Mar-26 A	0.00	0.00	0.00	100%	100%
DAM3-E-PS-E-0070	Low Voltage cables	2	12-Feb-26	14-Feb-26	14-Mar-26 A	14-Mar-26 A	0.00	0.00	0.00	100%	100%
DAM3-E-PS-E-0020	Wires	2	01-Feb-26	02-Feb-26	14-Mar-26 A	14-Mar-26 A	0.00	0.00	0.00	100%	100%
DAM3-E-PS-E-0040	Grounding system	2	05-Feb-26	07-Feb-26	14-Mar-26 A	14-Mar-26 A	0.00	0.00	0.00	100%	100%
DAM3-E-PS-E-0110	Disconnect switches	2	23-Feb-26	25-Feb-26	25-Mar-26 A	25-Mar-26 A	0.00	0.00	0.00	100%	100%
DAM3-E-PS-E-0080	Main distribution board (MDB)	2	15-Feb-26	16-Feb-26	19-Apr-26 A	19-Apr-26 A	0.00	0.00	0.00	100%	100%
DAM3-E-PS-E-0210	Distribution board for pump room	1	21-Mar-26	22-Mar-26	19-Apr-26 A	19-Apr-26 A	0.00	0.00	0.00	100%	100%
DAM3-E-PS-E-0090	Lighting panel board	2	17-Feb-26	19-Feb-26	19-Apr-26 A	19-Apr-26 A	0.00	0.00	0.00	100%	100%
DAM3-E-PS-E-0100	PP-AC panel	2	19-Feb-26	23-Feb-26	19-Apr-26 A	19-Apr-26 A	0.00	0.00	0.00	100%	100%
DAM3-E-PS-E-0060	HDPE ducts	2	10-Feb-26	11-Feb-26	20-Apr-26 A	20-Apr-26 A	0.00	0.00	0.00	100%	100%
DAM3-E-PS-E-0260	Main program system & controller	2	01-Apr-26	02-Apr-26	20-Apr-26 A	20-Apr-26 A	0.00	0.00	0.00	100%	100%
DAM3-E-PS-E-0270	PLC controller	2	04-Apr-26	05-Apr-26	20-Apr-26 A	20-Apr-26 A	0.00	0.00	0.00	100%	100%
EXTERNAL		14	25-Mar-26	09-Apr-26	10-Jun-26 A	10-Jun-26 A	0.00	0.00	0.00	0%	0%
DAM3-E-PS-EX-0010	Asphalt works	2	25-Mar-26	26-Mar-26	10-Jun-26 A	10-Jun-26 A	0.00	0.00	0.00	100%	100%
DAM3-E-PS-EX-0020	Concrete parking bumper	2	28-Mar-26	29-Mar-26	10-Jun-26 A	10-Jun-26 A	0.00	0.00	0.00	100%	100%
DAM3-E-PS-EX-0030	Road markings	2	30-Mar-26	31-Mar-26	10-Jun-26 A	10-Jun-26 A	0.00	0.00	0.00	100%	100%
DAM3-E-PS-EX-0040	Road signs	2	01-Apr-26	02-Apr-26	10-Jun-26 A	10-Jun-26 A	0.00	0.00	0.00	100%	100%
DAM3-E-PS-EX-0060	Interlock tiles	2	04-Apr-26	05-Apr-26	10-Jun-26 A	10-Jun-26 A	0.00	0.00	0.00	100%	100%
DAM3-E-PS-EX-0070	Curbstones	2	06-Apr-26	07-Apr-26	10-Jun-26 A	10-Jun-26 A	0.00	0.00	0.00	100%	100%
DAM3-E-PS-EX-0080	Gravel bedding	2	08-Apr-26	09-Apr-26	10-Jun-26 A	10-Jun-26 A	0.00	0.00	0.00	100%	100%
ENVIRONMETAL		75	29-Jan-26	16-Feb-26	03-Feb-26 A	03-Mar-26 A	0.00	0.00	0.00	0%	0%
DAM3-E-PS-EN-0080	UPVC pipes	2	15-Feb-26	16-Feb-26	03-Feb-26 A	03-Mar-26 A	0.00	0.00	0.00	100%	100%
DAM3-E-PS-EN-0010	HDPE pipes for fire system	2	29-Jan-26	31-Jan-26	05-Feb-26 A	05-Feb-26 A	0.00	0.00	0.00	100%	100%
DAM3-E-PS-EN-0030	HDPE pipes for water supply system	2	03-Feb-26	04-Feb-26	05-Feb-26 A	05-Feb-26 A	0.00	0.00	0.00	100%	100%
DAM3-E-PS-EN-0020	Directly buried gate valve for fire system	2	01-Feb-26	02-Feb-26	14-Feb-26 A	14-Feb-26 A	0.00	0.00	0.00	100%	100%
DAM3-E-PS-EN-0040	Directly buried gate valve for water system	2	05-Feb-26	07-Feb-26	14-Feb-26 A	14-Feb-26 A	0.00	0.00	0.00	100%	100%
DAM3-E-PS-EN-0050	Air valve	2	08-Feb-26	09-Feb-26	16-Feb-26 A	16-Feb-26 A	0.00	0.00	0.00	100%	100%

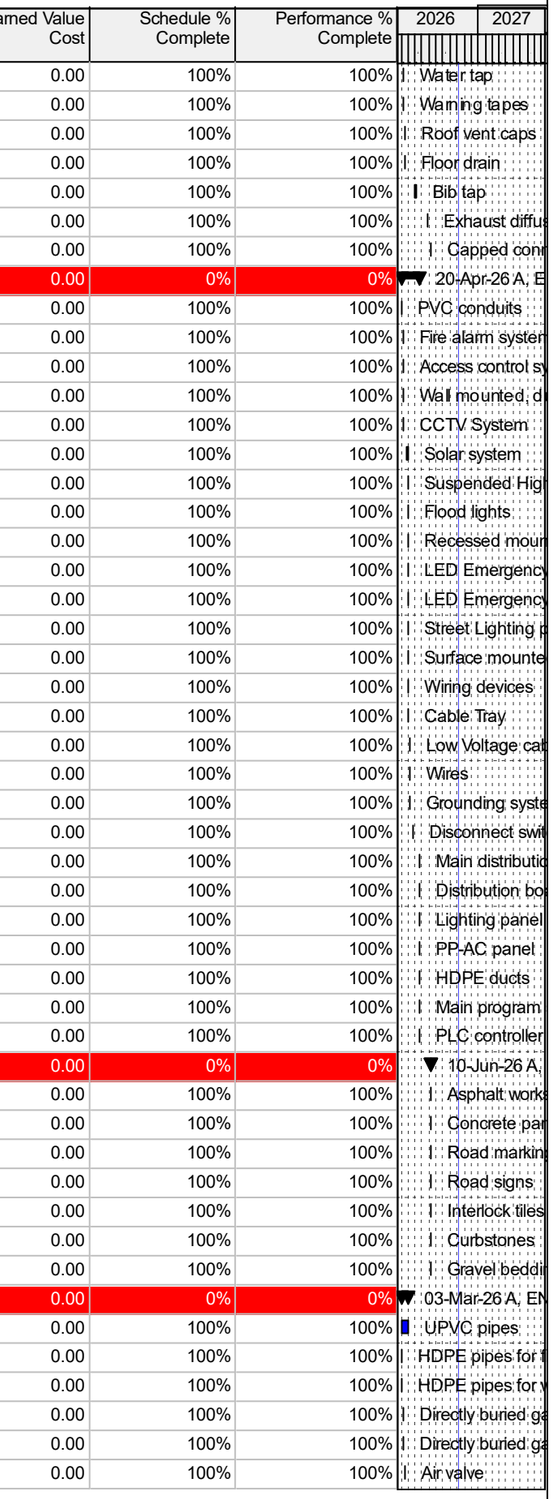

Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary

Date	Revision	Checked	Approved
06-Oct-26	Weekly Report		


Activity ID	Activity Name	Original Duration	BL Project Start	BL Project Finish	Start	Finish	Budgeted Total Cost	Planned Value Cost	Earned Value Cost	Schedule % Complete	Performance % Complete
DAM3-E-PS-EN-0060	Washout valve	2	10-Feb-26	11-Feb-26	16-Feb-26 A	16-Feb-26 A	0.00	0.00	0.00	100%	100%
DAM3-E-PS-EN-0070	Gate valve	2	12-Feb-26	14-Feb-26	16-Feb-26 A	16-Feb-26 A	0.00	0.00	0.00	100%	100%
REVIEW AND APPROVAL		138	25-Jan-26	12-Apr-26	15-Jan-26 A	11-Jun-26 A	0.00	0.00	0.00	0%	0%
STRUCTURAL		34	25-Jan-26	04-Feb-26	15-Jan-26 A	21-Jan-26 A	0.00	0.00	0.00	0%	0%
DAM3-E-PA-C-0010	Anti termite	2	25-Jan-26	26-Jan-26	15-Jan-26 A	20-Jan-26 A	0.00	0.00	0.00	100%	100%
DAM3-E-PA-C-0020	Concrete mix	2	27-Jan-26	28-Jan-26	15-Jan-26 A	20-Jan-26 A	0.00	0.00	0.00	100%	100%
DAM3-E-PA-C-0040	Bitumen paint	2	01-Feb-26	02-Feb-26	15-Jan-26 A	20-Jan-26 A	0.00	0.00	0.00	100%	100%
DAM3-E-PA-C-0050	Rebar	2	03-Feb-26	04-Feb-26	15-Jan-26 A	20-Jan-26 A	0.00	0.00	0.00	100%	100%
DAM3-E-PA-C-0030	Polyethylene sheet	5	29-Jan-26	31-Jan-26	19-Jan-26 A	21-Jan-26 A	0.00	0.00	0.00	100%	100%
ARCHITECTURAL		104	27-Jan-26	04-Mar-26	08-Feb-26 A	11-Jun-26 A	0.00	0.00	0.00	0%	0%
DAM3-E-PA-A-0040	Concrete masonry unit (CMU)	2	29-Jan-26	31-Jan-26	08-Feb-26 A	09-Feb-26 A	0.00	0.00	0.00	100%	100%
DAM3-E-PA-A-0130	Windows	2	10-Feb-26	11-Feb-26	08-Feb-26 A	09-Feb-26 A	0.00	0.00	0.00	100%	100%
DAM3-E-PA-A-0200	Aluminum Composite Panel	2	25-Feb-26	28-Feb-26	09-Feb-26 A	10-Feb-26 A	0.00	0.00	0.00	100%	100%
DAM3-E-PA-A-0120	Doors	2	08-Feb-26	09-Feb-26	16-Feb-26 A	17-Feb-26 A	0.00	0.00	0.00	100%	100%
DAM3-E-PA-A-0050	Steel ladder	2	01-Feb-26	02-Feb-26	17-Feb-26 A	19-Feb-26 A	0.00	0.00	0.00	100%	100%
DAM3-E-PA-A-0020	PES -Steel Structure	2	27-Jan-26	28-Jan-26	17-Feb-26 A	19-Feb-26 A	0.00	0.00	0.00	100%	100%
DAM3-E-PA-A-0190	Gypsum board	2	23-Feb-26	25-Feb-26	24-Feb-26 A	12-Apr-26 A	0.00	0.00	0.00	100%	100%
DAM3-E-PA-A-0140	Ceramic tiles	2	12-Feb-26	14-Feb-26	25-Mar-26 A	26-Mar-26 A	0.00	0.00	0.00	100%	100%
DAM3-E-PA-A-0180	Interni paint	2	19-Feb-26	23-Feb-26	25-Mar-26 A	26-Mar-26 A	0.00	0.00	0.00	100%	100%
DAM3-E-PA-A-0170	Epoxy paint	2	17-Feb-26	19-Feb-26	20-Apr-26 A	21-Apr-26 A	0.00	0.00	0.00	100%	100%
DAM3-E-PA-A-0150	Granite strip	2	15-Feb-26	16-Feb-26	03-May-26 A	04-May-26 A	0.00	0.00	0.00	100%	100%
DAM3-E-PA-A-0060	Steel gratings	2	03-Feb-26	04-Feb-26	19-May-26 A	20-May-26 A	0.00	0.00	0.00	100%	100%
DAM3-E-PA-A-0230	Steel fence and gates	2	01-Mar-26	02-Mar-26	20-May-26 A	21-May-26 A	0.00	0.00	0.00	100%	100%
DAM3-E-PA-A-0070	Steel rails	2	05-Feb-26	07-Feb-26	10-Jun-26 A	11-Jun-26 A	0.00	0.00	0.00	100%	100%
DAM3-E-PA-A-0240	Identification sign; ID01 & ID02	2	03-Mar-26	04-Mar-26	10-Jun-26 A	11-Jun-26 A	0.00	0.00	0.00	100%	100%
MECHANICAL		98	29-Jan-26	12-Apr-26	24-Jan-26 A	11-Jun-26 A	0.00	0.00	0.00	0%	0%
DAM3-E-PA-M-0340	GRP tank	2	06-Apr-26	07-Apr-26	24-Jan-26 A	16-Feb-26 A	0.00	0.00	0.00	100%	100%
DAM3-E-PA-M-0250	Inline exhaust fans	2	25-Mar-26	26-Mar-26	02-Feb-26 A	17-Feb-26 A	0.00	0.00	0.00	100%	100%
DAM3-E-PA-M-0260	Wall propeller type exhaust fans	2	28-Mar-26	29-Mar-26	02-Feb-26 A	17-Feb-26 A	0.00	0.00	0.00	100%	100%
DAM3-E-PA-M-0280	Fire fighting valves	2	01-Apr-26	02-Apr-26	02-Feb-26 A	03-Feb-26 A	0.00	0.00	0.00	100%	100%
DAM3-E-PA-M-0350	Water supply valves	2	08-Apr-26	09-Apr-26	02-Feb-26 A	03-Feb-26 A	0.00	0.00	0.00	100%	100%
DAM3-E-PA-M-0030	PPR pipes	2	01-Feb-26	02-Feb-26	03-Feb-26 A	04-Feb-26 A	0.00	0.00	0.00	100%	100%
DAM3-E-PA-M-0270	Fire pumps	2	30-Mar-26	31-Mar-26	03-Feb-26 A	04-Feb-26 A	0.00	0.00	0.00	100%	100%
DAM3-E-PA-M-0330	Booster pump	2	04-Apr-26	05-Apr-26	03-Feb-26 A	04-Feb-26 A	0.00	0.00	0.00	100%	100%
DAM3-E-PA-M-0070	U/G HDPE pipes	2	10-Feb-26	11-Feb-26	04-Feb-26 A	05-Feb-26 A	0.00	0.00	0.00	100%	100%
DAM3-E-PA-M-0090	Fire hose cabinet	2	12-Feb-26	14-Feb-26	04-Feb-26 A	05-Feb-26 A	0.00	0.00	0.00	100%	100%
DAM3-E-PA-M-0160	UPVC pipes	2	01-Mar-26	02-Mar-26	04-Feb-26 A	05-Feb-26 A	0.00	0.00	0.00	100%	100%
DAM3-E-PA-M-0200	Electric water heater	2	10-Mar-26	11-Mar-26	05-Feb-26 A	07-Feb-26 A	0.00	0.00	0.00	100%	100%
DAM3-E-PA-M-0210	Western water closet	2	12-Mar-26	14-Mar-26	05-Feb-26 A	07-Feb-26 A	0.00	0.00	0.00	100%	100%
DAM3-E-PA-M-0240	Lavatory / wash basin	2	23-Mar-26	24-Mar-26	05-Feb-26 A	07-Feb-26 A	0.00	0.00	0.00	100%	100%
DAM3-E-PA-M-0190	Gully trap	2	08-Mar-26	09-Mar-26	07-Feb-26 A	08-Feb-26 A	0.00	0.00	0.00	100%	100%
DAM3-E-PA-M-0230	Toilet Fittings	2	21-Mar-26	22-Mar-26	07-Feb-26 A	08-Feb-26 A	0.00	0.00	0.00	100%	100%
DAM3-E-PA-M-0010	Seamless black steel or ERW pipes	2	29-Jan-26	31-Jan-26	08-Feb-26 A	09-Feb-26 A	0.00	0.00	0.00	100%	100%
DAM3-E-PA-M-0100	Automatic air release valve	2	15-Feb-26	16-Feb-26	08-Feb-26 A	09-Feb-26 A	0.00	0.00	0.00	100%	100%
DAM3-E-PA-M-0110	OS & Y gate valve	2	17-Feb-26	19-Feb-26	08-Feb-26 A	09-Feb-26 A	0.00	0.00	0.00	100%	100%
DAM3-E-PA-M-0120	Fire alarm check valve	2	19-Feb-26	23-Feb-26	08-Feb-26 A	09-Feb-26 A	0.00	0.00	0.00	100%	100%
DAM3-E-PA-M-0040	HVAC duct	2	03-Feb-26	04-Feb-26	09-Feb-26 A	10-Feb-26 A	0.00	0.00	0.00	100%	100%
DAM3-E-PA-M-0050	Flexible duct	2	05-Feb-26	07-Feb-26	09-Feb-26 A	10-Feb-26 A	0.00	0.00	0.00	100%	100%
DAM3-E-PA-M-0140	Ball valve	2	23-Feb-26	25-Feb-26	11-Feb-26 A	11-Feb-26 A	0.00	0.00	0.00	100%	100%

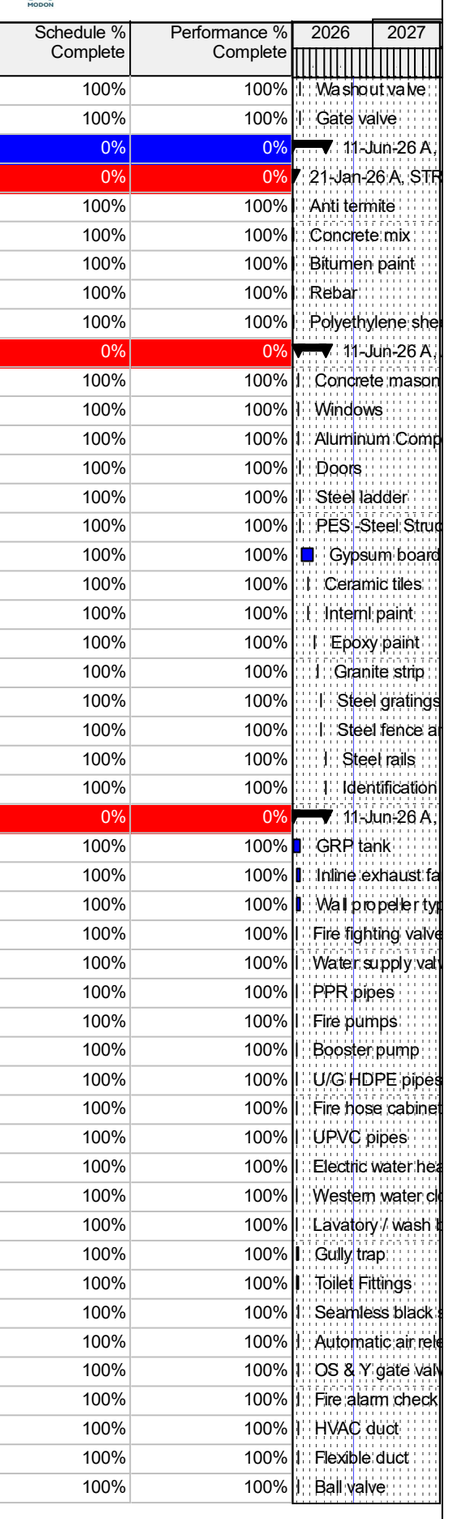

Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary

Date	Revision	Checked	Approved
06-Oct-26	Weekly Report		

Activity ID	Activity Name	Original Duration	BL Project Start	BL Project Finish	Start	Finish	Budgeted Total Cost	Planned Value Cost	Earned Value Cost	Schedule % Complete	Performance % Complete
DAM3-E-PA-M-0320	Water tap	2	11-Apr-26	12-Apr-26	11-Feb-26 A	12-Feb-26 A	0.00	0.00	0.00	100%	100%
DAM3-E-PA-M-0080	Warning tapes	2	10-Feb-26	11-Feb-26	14-Feb-26 A	15-Feb-26 A	0.00	0.00	0.00	100%	100%
DAM3-E-PA-M-0170	Roof vent caps	2	03-Mar-26	04-Mar-26	16-Feb-26 A	17-Feb-26 A	0.00	0.00	0.00	100%	100%
DAM3-E-PA-M-0180	Floor drain	2	05-Mar-26	07-Mar-26	16-Feb-26 A	17-Feb-26 A	0.00	0.00	0.00	100%	100%
DAM3-E-PA-M-0220	Bib tap	2	15-Mar-26	16-Mar-26	06-Apr-26 A	07-Apr-26 A	0.00	0.00	0.00	100%	100%
DAM3-E-PA-M-0060	Exhaust diffuser	2	08-Feb-26	09-Feb-26	27-May-26 A	28-May-26 A	0.00	0.00	0.00	100%	100%
DAM3-E-PA-M-0150	Capped connection	2	25-Feb-26	28-Feb-26	10-Jun-26 A	11-Jun-26 A	0.00	0.00	0.00	100%	100%
ELECTRICAL		85	01-Feb-26	07-Apr-26	07-Feb-26 A	21-Apr-26 A	0.00	0.00	0.00	0%	0%
DAM3-E-PA-E-0010	PVC conduits	2	01-Feb-26	02-Feb-26	07-Feb-26 A	08-Feb-26 A	0.00	0.00	0.00	100%	100%
DAM3-E-PA-E-0180	Fire alarm system	2	15-Mar-26	16-Mar-26	09-Feb-26 A	10-Feb-26 A	0.00	0.00	0.00	100%	100%
DAM3-E-PA-E-0240	Access control system	2	30-Mar-26	31-Mar-26	09-Feb-26 A	10-Feb-26 A	0.00	0.00	0.00	100%	100%
DAM3-E-PA-E-0170	Wall mounted, duplex, telephone and data outlet	2	12-Mar-26	14-Mar-26	11-Feb-26 A	14-Feb-26 A	0.00	0.00	0.00	100%	100%
DAM3-E-PA-E-0230	CCTV System	2	28-Mar-26	29-Mar-26	11-Feb-26 A	14-Feb-26 A	0.00	0.00	0.00	100%	100%
DAM3-E-PA-E-0250	Solar system	2	01-Apr-26	02-Apr-26	24-Feb-26 A	02-Mar-26 A	0.00	0.00	0.00	100%	100%
DAM3-E-PA-E-0120	Suspended High Bay LED lights	2	01-Mar-26	02-Mar-26	01-Mar-26 A	02-Mar-26 A	0.00	0.00	0.00	100%	100%
DAM3-E-PA-E-0130	Flood lights	2	03-Mar-26	04-Mar-26	01-Mar-26 A	02-Mar-26 A	0.00	0.00	0.00	100%	100%
DAM3-E-PA-E-0140	Recessed mounted LED downlight	2	05-Mar-26	07-Mar-26	01-Mar-26 A	02-Mar-26 A	0.00	0.00	0.00	100%	100%
DAM3-E-PA-E-0150	LED Emergency Lights wall mounted	2	08-Mar-26	09-Mar-26	01-Mar-26 A	02-Mar-26 A	0.00	0.00	0.00	100%	100%
DAM3-E-PA-E-0160	LED Emergency Exit Light	2	10-Mar-26	11-Mar-26	01-Mar-26 A	02-Mar-26 A	0.00	0.00	0.00	100%	100%
DAM3-E-PA-E-0200	Street Lighting poles	2	21-Mar-26	22-Mar-26	01-Mar-26 A	02-Mar-26 A	0.00	0.00	0.00	100%	100%
DAM3-E-PA-E-0220	Surface mounted lights	2	25-Mar-26	26-Mar-26	01-Mar-26 A	02-Mar-26 A	0.00	0.00	0.00	100%	100%
DAM3-E-PA-E-0050	Wiring devices	2	10-Feb-26	11-Feb-26	03-Mar-26 A	04-Mar-26 A	0.00	0.00	0.00	100%	100%
DAM3-E-PA-E-0030	Cable Tray	2	05-Feb-26	07-Feb-26	03-Mar-26 A	04-Mar-26 A	0.00	0.00	0.00	100%	100%
DAM3-E-PA-E-0070	Low Voltage cables	2	15-Feb-26	16-Feb-26	14-Mar-26 A	15-Mar-26 A	0.00	0.00	0.00	100%	100%
DAM3-E-PA-E-0020	Wires	2	03-Feb-26	04-Feb-26	14-Mar-26 A	15-Mar-26 A	0.00	0.00	0.00	100%	100%
DAM3-E-PA-E-0040	Grounding system	2	08-Feb-26	09-Feb-26	14-Mar-26 A	15-Mar-26 A	0.00	0.00	0.00	100%	100%
DAM3-E-PA-E-0110	Disconnect switches	2	25-Feb-26	28-Feb-26	25-Mar-26 A	26-Mar-26 A	0.00	0.00	0.00	100%	100%
DAM3-E-PA-E-0080	Main distribution board (MDB)	2	17-Feb-26	19-Feb-26	19-Apr-26 A	20-Apr-26 A	0.00	0.00	0.00	100%	100%
DAM3-E-PA-E-0210	Distribution board for pump room	2	23-Mar-26	24-Mar-26	19-Apr-26 A	20-Apr-26 A	0.00	0.00	0.00	100%	100%
DAM3-E-PA-E-0090	Lighting panel board	2	19-Feb-26	23-Feb-26	19-Apr-26 A	20-Apr-26 A	0.00	0.00	0.00	100%	100%
DAM3-E-PA-E-0100	PP-AC panel	2	23-Feb-26	25-Feb-26	19-Apr-26 A	20-Apr-26 A	0.00	0.00	0.00	100%	100%
DAM3-E-PA-E-0060	HDPE ducts	2	12-Feb-26	14-Feb-26	20-Apr-26 A	21-Apr-26 A	0.00	0.00	0.00	100%	100%
DAM3-E-PA-E-0260	Main program system & controller	2	04-Apr-26	05-Apr-26	20-Apr-26 A	21-Apr-26 A	0.00	0.00	0.00	100%	100%
DAM3-E-PA-E-0270	PLC controller	2	06-Apr-26	07-Apr-26	20-Apr-26 A	21-Apr-26 A	0.00	0.00	0.00	100%	100%
EXTERNAL		14	28-Mar-26	12-Apr-26	09-Jun-26 A	10-Jun-26 A	0.00	0.00	0.00	0%	0%
DAM3-E-PA-EX-0010	Asphalt works	2	28-Mar-26	29-Mar-26	09-Jun-26 A	10-Jun-26 A	0.00	0.00	0.00	100%	100%
DAM3-E-PA-EX-0020	Concrete parking bumper	2	30-Mar-26	31-Mar-26	09-Jun-26 A	10-Jun-26 A	0.00	0.00	0.00	100%	100%
DAM3-E-PA-EX-0030	Road markings	2	01-Apr-26	02-Apr-26	09-Jun-26 A	10-Jun-26 A	0.00	0.00	0.00	100%	100%
DAM3-E-PA-EX-0040	Road signs	2	04-Apr-26	05-Apr-26	09-Jun-26 A	10-Jun-26 A	0.00	0.00	0.00	100%	100%
DAM3-E-PA-EX-0060	Interlock tiles	2	06-Apr-26	07-Apr-26	09-Jun-26 A	10-Jun-26 A	0.00	0.00	0.00	100%	100%
DAM3-E-PA-EX-0070	Curbstones	2	08-Apr-26	09-Apr-26	09-Jun-26 A	10-Jun-26 A	0.00	0.00	0.00	100%	100%
DAM3-E-PA-EX-0080	Gravel bedding	2	11-Apr-26	12-Apr-26	09-Jun-26 A	10-Jun-26 A	0.00	0.00	0.00	100%	100%
ENVIRONMETAL		73	01-Feb-26	19-Feb-26	03-Feb-26 A	17-Feb-26 A	0.00	0.00	0.00	0%	0%
DAM3-E-PA-EN-0080	UPVC pipes	2	17-Feb-26	19-Feb-26	03-Feb-26 A	04-Feb-26 A	0.00	0.00	0.00	100%	100%
DAM3-E-PA-EN-0010	HDPE pipes for fire system	2	01-Feb-26	02-Feb-26	05-Feb-26 A	07-Feb-26 A	0.00	0.00	0.00	100%	100%
DAM3-E-PA-EN-0030	HDPE pipes for water supply system	2	05-Feb-26	07-Feb-26	05-Feb-26 A	07-Feb-26 A	0.00	0.00	0.00	100%	100%
DAM3-E-PA-EN-0020	Directly buried gate valve for fire system	2	03-Feb-26	04-Feb-26	14-Feb-26 A	15-Feb-26 A	0.00	0.00	0.00	100%	100%
DAM3-E-PA-EN-0040	Directly buried gate valve for water system	2	08-Feb-26	09-Feb-26	14-Feb-26 A	15-Feb-26 A	0.00	0.00	0.00	100%	100%
DAM3-E-PA-EN-0050	Air valve	2	10-Feb-26	11-Feb-26	16-Feb-26 A	17-Feb-26 A	0.00	0.00	0.00	100%	100%

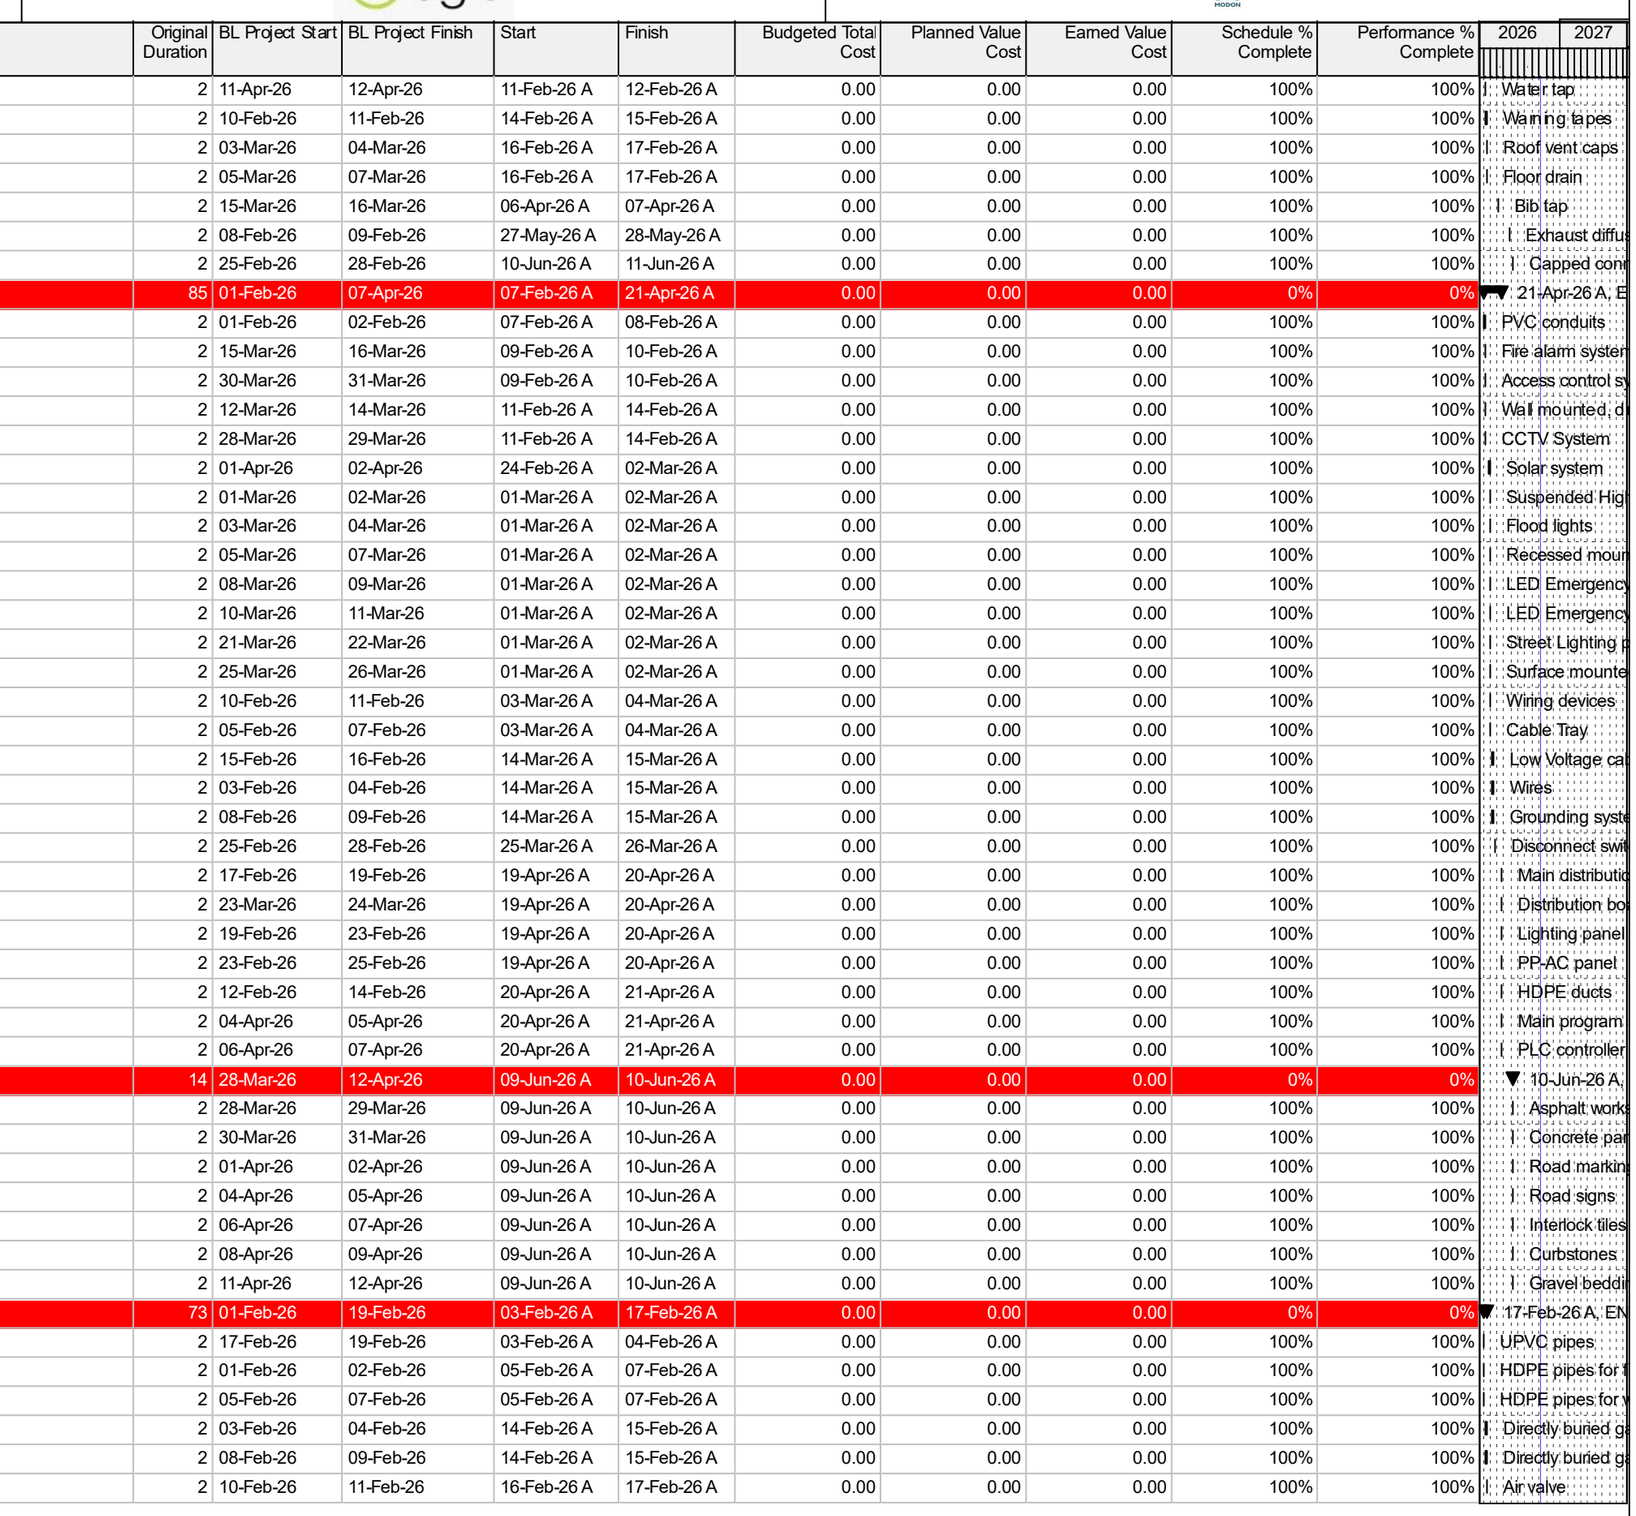

Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary

Date	Revision	Checked	Approved
06-Oct-26	Weekly Report		

Activity ID	Activity Name	Original Duration	BL Project Start	BL Project Finish	Start	Finish	Budgeted Total Cost	Planned Value Cost	Earned Value Cost	Schedule % Complete	Performance % Complete	2026 2027
DAM3-E-PA-EN-0060	Washout valve	2	12-Feb-26	14-Feb-26	16-Feb-26 A	17-Feb-26 A	0.00	0.00	0.00	100%	100%	Washout valve
DAM3-E-PA-EN-0070	Gate valve	2	15-Feb-26	16-Feb-26	16-Feb-26 A	17-Feb-26 A	0.00	0.00	0.00	100%	100%	Gate valve
MATERIAL SUBMITTAL		108	27-Jan-26	20-Apr-26	15-Jan-26 A	14-Jun-26 A	2,879,895.75	2,879,895.75	2,879,895.75	100%	100%	14-Jun-26 A,
PREPARATION AND SUBMITTAL		108	27-Jan-26	14-Apr-26	15-Jan-26 A	13-Jun-26 A	0.00	0.00	0.00	0%	0%	13-Jun-26 A,
STRUCTURAL		10	27-Jan-26	07-Feb-26	15-Jan-26 A	14-Mar-26 A	0.00	0.00	0.00	0%	0%	14-Mar-26 A, ST
DAM3-E-MS-C-0020	Concrete mix	2	29-Jan-26	31-Jan-26	15-Jan-26 A	15-Jan-26 A	0.00	0.00	0.00	100%	100%	Concrete mix
DAM3-E-MS-C-0030	Polyethylene sheet	2	01-Feb-26	02-Feb-26	22-Jan-26 A	22-Jan-26 A	0.00	0.00	0.00	100%	100%	Polyethylene she
DAM3-E-MS-C-0040	Bitumen paint	2	03-Feb-26	04-Feb-26	22-Jan-26 A	22-Jan-26 A	0.00	0.00	0.00	100%	100%	Bitumen paint
DAM3-E-MS-C-0050	Rebar	2	05-Feb-26	07-Feb-26	22-Jan-26 A	22-Jan-26 A	0.00	0.00	0.00	100%	100%	Rebar
DAM3-E-MS-C-0010	Anti termite	2	27-Jan-26	28-Jan-26	14-Mar-26 A	14-Mar-26 A	0.00	0.00	0.00	100%	100%	Anti termite
ARCHITECTURAL		100	29-Jan-26	07-Mar-26	07-Feb-26 A	13-Jun-26 A	0.00	0.00	0.00	0%	0%	13-Jun-26 A,
DAM3-E-MS-A-0030	Steel ladder	2	03-Feb-26	04-Feb-26	07-Feb-26 A	07-Feb-26 A	0.00	0.00	0.00	100%	100%	Steel ladder
DAM3-E-MS-A-1700	PES -Steel Structure	2	29-Jan-26	31-Jan-26	07-Feb-26 A	07-Feb-26 A	0.00	0.00	0.00	100%	100%	PES -Steel Struc
DAM3-E-MS-A-0100	Doors	2	10-Feb-26	11-Feb-26	19-Feb-26 A	19-Feb-26 A	0.00	0.00	0.00	100%	100%	Doors
DAM3-E-MS-A-0110	Windows	2	12-Feb-26	14-Feb-26	19-Feb-26 A	19-Feb-26 A	0.00	0.00	0.00	100%	100%	Windows
DAM3-E-MS-A-1720	Aluminum Composite Panel	2	01-Mar-26	02-Mar-26	19-Feb-26 A	19-Feb-26 A	0.00	0.00	0.00	100%	100%	Aluminum Comp
DAM3-E-MS-A-0160	Interni paint	2	23-Feb-26	25-Feb-26	29-Mar-26 A	29-Mar-26 A	0.00	0.00	0.00	100%	100%	Interni paint
DAM3-E-MS-A-0120	Ceramic tiles	2	15-Feb-26	16-Feb-26	30-Mar-26 A	30-Mar-26 A	0.00	0.00	0.00	100%	100%	Ceramic tiles
DAM3-E-MS-A-0170	Gypsum board	2	25-Feb-26	28-Feb-26	19-Apr-26 A	19-Apr-26 A	0.00	0.00	0.00	100%	100%	Gypsum board
DAM3-E-MS-A-0020	Concrete masonry unit (CMU)	2	01-Feb-26	02-Feb-26	26-Apr-26 A	26-Apr-26 A	0.00	0.00	0.00	100%	100%	Concrete mas
DAM3-E-MS-A-0150	Epoxy paint	2	19-Feb-26	23-Feb-26	29-Apr-26 A	29-Apr-26 A	0.00	0.00	0.00	100%	100%	Epoxy paint
DAM3-E-MS-A-0130	Granite strip	2	17-Feb-26	19-Feb-26	09-May-26 A	09-May-26 A	0.00	0.00	0.00	100%	100%	Granite strip
DAM3-E-MS-A-0040	Steel gratings	2	05-Feb-26	07-Feb-26	21-May-26 A	21-May-26 A	0.00	0.00	0.00	100%	100%	Steel gratings
DAM3-E-MS-A-1750	Steel fence and gates	2	03-Mar-26	04-Mar-26	23-May-26 A	23-May-26 A	0.00	0.00	0.00	100%	100%	Steel fence a
DAM3-E-MS-A-0050	Steel rails	2	08-Feb-26	09-Feb-26	13-Jun-26 A	13-Jun-26 A	0.00	0.00	0.00	100%	100%	Steel rails
DAM3-E-MS-A-1760	Identification sign; ID01 & ID02	2	05-Mar-26	07-Mar-26	13-Jun-26 A	13-Jun-26 A	0.00	0.00	0.00	100%	100%	Identification
MECHANICAL		98	01-Feb-26	14-Apr-26	05-Feb-26 A	13-Jun-26 A	0.00	0.00	0.00	0%	0%	13-Jun-26 A,
DAM3-E-MS-M-0080	PPR pipes	2	03-Feb-26	04-Feb-26	05-Feb-26 A	05-Feb-26 A	0.00	0.00	0.00	100%	100%	PPR pipes
DAM3-E-MS-M-0250	Fire pumps	2	01-Apr-26	02-Apr-26	05-Feb-26 A	05-Feb-26 A	0.00	0.00	0.00	100%	100%	Fire pumps
DAM3-E-MS-M-0310	Booster pump	2	06-Apr-26	07-Apr-26	05-Feb-26 A	05-Feb-26 A	0.00	0.00	0.00	100%	100%	Booster pump
DAM3-E-MS-M-0010	U/G HDPE pipes	2	12-Feb-26	14-Feb-26	07-Feb-26 A	07-Feb-26 A	0.00	0.00	0.00	100%	100%	U/G HDPE pipes
DAM3-E-MS-M-0030	Fire hose cabinet	2	15-Feb-26	16-Feb-26	07-Feb-26 A	07-Feb-26 A	0.00	0.00	0.00	100%	100%	Fire hose cabinet
DAM3-E-MS-M-0110	UPVC pipes	2	03-Mar-26	04-Mar-26	07-Feb-26 A	07-Feb-26 A	0.00	0.00	0.00	100%	100%	UPVC pipes
DAM3-E-MS-M-0150	Electric water heater	2	12-Mar-26	14-Mar-26	08-Feb-26 A	08-Feb-26 A	0.00	0.00	0.00	100%	100%	Electric water hea
DAM3-E-MS-M-0160	Western water closet	2	15-Mar-26	16-Mar-26	08-Feb-26 A	08-Feb-26 A	0.00	0.00	0.00	100%	100%	Western water cl
DAM3-E-MS-M-0190	Lavatory / wash basin	2	25-Mar-26	26-Mar-26	08-Feb-26 A	08-Feb-26 A	0.00	0.00	0.00	100%	100%	Lavatory / wash
DAM3-E-MS-M-0140	Gully trap	2	10-Mar-26	11-Mar-26	09-Feb-26 A	09-Feb-26 A	0.00	0.00	0.00	100%	100%	Gully trap
DAM3-E-MS-M-0180	Toilet Fittings	2	23-Mar-26	24-Mar-26	09-Feb-26 A	09-Feb-26 A	0.00	0.00	0.00	100%	100%	Toilet Fittings
DAM3-E-MS-M-0020	Seamless black steel or ERW pipes	2	01-Feb-26	02-Feb-26	10-Feb-26 A	10-Feb-26 A	0.00	0.00	0.00	100%	100%	Seamless black s
DAM3-E-MS-M-0040	Automatic air release valve	2	17-Feb-26	19-Feb-26	10-Feb-26 A	10-Feb-26 A	0.00	0.00	0.00	100%	100%	Automatic air rele
DAM3-E-MS-M-0050	OS & Y gate valve	2	19-Feb-26	23-Feb-26	10-Feb-26 A	10-Feb-26 A	0.00	0.00	0.00	100%	100%	OS & Y gate valv
DAM3-E-MS-M-0060	Fire alarm check valve	2	23-Feb-26	25-Feb-26	10-Feb-26 A	10-Feb-26 A	0.00	0.00	0.00	100%	100%	Fire alarm check
DAM3-E-MS-M-0270	Fire fighting valves	2	04-Apr-26	05-Apr-26	10-Feb-26 A	10-Feb-26 A	0.00	0.00	0.00	100%	100%	Fire fighting valve
DAM3-E-MS-M-0330	Water supply valves	2	11-Apr-26	12-Apr-26	10-Feb-26 A	10-Feb-26 A	0.00	0.00	0.00	100%	100%	Water supply val
DAM3-E-MS-M-0090	Ball valve	2	25-Feb-26	28-Feb-26	14-Feb-26 A	14-Feb-26 A	0.00	0.00	0.00	100%	100%	Ball valve
DAM3-E-MS-M-0170	Bib tap	2	21-Mar-26	22-Mar-26	14-Feb-26 A	14-Mar-26 A	0.00	0.00	0.00	100%	100%	Bib tap
DAM3-E-MS-M-3410	Water tap	2	13-Apr-26	14-Apr-26	14-Feb-26 A	14-Feb-26 A	0.00	0.00	0.00	100%	100%	Water tap
DAM3-E-MS-M-0120	Roof vent caps	2	05-Mar-26	07-Mar-26	16-Feb-26 A	16-Feb-26 A	0.00	0.00	0.00	100%	100%	Roof vent caps
DAM3-E-MS-M-0130	Floor drain	2	08-Mar-26	09-Mar-26	16-Feb-26 A	16-Feb-26 A	0.00	0.00	0.00	100%	100%	Floor drain

Activity ID	Activity Name	Original Duration	BL Project Start	BL Project Finish	Start	Finish	Budgeted Total Cost	Planned Value Cost	Earned Value Cost	Schedule % Complete	Performance % Complete	2026	2027
DAM3-E-MS-M-0340	Warning tapes	2	12-Feb-26	14-Feb-26	16-Feb-26 A	16-Feb-26 A	0.00	0.00	0.00	100%	100%	Warning tapes	
DAM3-E-MS-M-0320	GRP tank	2	08-Apr-26	09-Apr-26	02-Mar-26 A	02-Mar-26 A	0.00	0.00	0.00	100%	100%	GRP tank	
DAM3-E-MS-M-0220	HVAC duct	2	05-Feb-26	07-Feb-26	04-Mar-26 A	04-Mar-26 A	0.00	0.00	0.00	100%	100%	HVAC duct	
DAM3-E-MS-M-0230	Flexible duct	2	08-Feb-26	09-Feb-26	04-Mar-26 A	04-Mar-26 A	0.00	0.00	0.00	100%	100%	Flexible duct	
DAM3-E-MS-M-0200	Inline exhaust fans	2	28-Mar-26	29-Mar-26	18-Mar-26 A	18-Mar-26 A	0.00	0.00	0.00	100%	100%	Inline exhaust f	
DAM3-E-MS-M-0210	Wall propeller type exhaust fans	2	30-Mar-26	31-Mar-26	18-Mar-26 A	18-Mar-26 A	0.00	0.00	0.00	100%	100%	Wall propeller ty	
DAM3-E-MS-M-0240	Exhaust diffuser	2	10-Feb-26	11-Feb-26	01-Jun-26 A	01-Jun-26 A	0.00	0.00	0.00	100%	100%	Exhaust diffu	
DAM3-E-MS-M-0100	Capped connection	2	01-Mar-26	02-Mar-26	13-Jun-26 A	13-Jun-26 A	0.00	0.00	0.00	100%	100%	Capped conn	
ELECTRICAL		69	03-Feb-26	09-Apr-26	09-Feb-26 A	30-Apr-26 A	0.00	0.00	0.00	0%	0%	30-Apr-26 A, E	
DAM3-E-MS-E-0040	PVC conduits	2	03-Feb-26	04-Feb-26	09-Feb-26 A	09-Feb-26 A	0.00	0.00	0.00	100%	100%	PVC conduits	
DAM3-E-MS-E-0130	Fire alarm system	2	21-Mar-26	22-Mar-26	11-Feb-26 A	11-Feb-26 A	0.00	0.00	0.00	100%	100%	Fire alarm systen	
DAM3-E-MS-E-0240	Access control system	2	01-Apr-26	02-Apr-26	11-Feb-26 A	11-Feb-26 A	0.00	0.00	0.00	100%	100%	Access control sy	
DAM3-E-MS-E-0060	Suspended High Bay LED lights	2	03-Mar-26	04-Mar-26	03-Mar-26 A	03-Mar-26 A	0.00	0.00	0.00	100%	100%	Suspended Hig	
DAM3-E-MS-E-0070	Flood lights	2	05-Mar-26	07-Mar-26	03-Mar-26 A	03-Mar-26 A	0.00	0.00	0.00	100%	100%	Flood lights	
DAM3-E-MS-E-0080	Recessed mounted LED downlight	2	08-Mar-26	09-Mar-26	03-Mar-26 A	03-Mar-26 A	0.00	0.00	0.00	100%	100%	Recessed moun	
DAM3-E-MS-E-0090	LED Emergency Lights wall mounted	2	10-Mar-26	11-Mar-26	03-Mar-26 A	03-Mar-26 A	0.00	0.00	0.00	100%	100%	LED Emergency	
DAM3-E-MS-E-0100	LED Emergency Exit Light	2	12-Mar-26	14-Mar-26	03-Mar-26 A	03-Mar-26 A	0.00	0.00	0.00	100%	100%	LED Emergency	
DAM3-E-MS-E-0190	Surface mounted lights	2	28-Mar-26	29-Mar-26	03-Mar-26 A	03-Mar-26 A	0.00	0.00	0.00	100%	100%	Surface mounte	
DAM3-E-MS-E-0250	Solar system	2	04-Apr-26	05-Apr-26	03-Mar-26 A	03-Mar-26 A	0.00	0.00	0.00	100%	100%	Solar system	
DAM3-E-MS-E-0170	Street Lighting poles	2	23-Mar-26	24-Mar-26	04-Mar-26 A	04-Mar-26 A	0.00	0.00	0.00	100%	100%	Street Lighting p	
DAM3-E-MS-E-0140	Wiring devices	2	12-Feb-26	14-Feb-26	07-Mar-26 A	07-Mar-26 A	0.00	0.00	0.00	100%	100%	Wiring devices	
DAM3-E-MS-E-210	Cable Tray	2	08-Feb-26	09-Feb-26	07-Mar-26 A	07-Mar-26 A	0.00	0.00	0.00	100%	100%	Cable Tray	
DAM3-E-MS-E-0010	Low Voltage cables	2	17-Feb-26	19-Feb-26	16-Mar-26 A	16-Mar-26 A	0.00	0.00	0.00	100%	100%	Low Voltage ca	
DAM3-E-MS-E-0050	Wires	2	05-Feb-26	07-Feb-26	16-Mar-26 A	16-Mar-26 A	0.00	0.00	0.00	100%	100%	Wires	
DAM3-E-MS-E-0120	Grounding system	2	10-Feb-26	11-Feb-26	16-Mar-26 A	16-Mar-26 A	0.00	0.00	0.00	100%	100%	Grounding syste	
DAM3-E-MS-E-0230	CCTV System	2	30-Mar-26	31-Mar-26	28-Mar-26 A	28-Mar-26 A	0.00	0.00	0.00	100%	100%	CCTV System	
DAM3-E-MS-E-0030	Disconnect switches	2	01-Mar-26	02-Mar-26	29-Mar-26 A	29-Mar-26 A	0.00	0.00	0.00	100%	100%	Disconnect swi	
DAM3-E-MS-E-0110	Wall mounted, duplex, telephone and data outlet	1	15-Mar-26	16-Mar-26	29-Mar-26 A	29-Mar-26 A	0.00	0.00	0.00	100%	100%	Wall mounted,	
DAM3-E-MS-E-0020	Main distribution board (MDB)	2	19-Feb-26	23-Feb-26	26-Apr-26 A	26-Apr-26 A	0.00	0.00	0.00	100%	100%	Main distributio	
DAM3-E-MS-E-0180	Distribution board for pump room	2	25-Mar-26	26-Mar-26	26-Apr-26 A	26-Apr-26 A	0.00	0.00	0.00	100%	100%	Distribution bo	
DAM3-E-MS-E-190	Lighting panel board	2	23-Feb-26	25-Feb-26	26-Apr-26 A	26-Apr-26 A	0.00	0.00	0.00	100%	100%	Lighting panel	
DAM3-E-MS-E-200	PP-AC panel	2	25-Feb-26	28-Feb-26	26-Apr-26 A	26-Apr-26 A	0.00	0.00	0.00	100%	100%	PP-AC panel	
DAM3-E-MS-E-0160	HDPE ducts	2	15-Feb-26	16-Feb-26	30-Apr-26 A	30-Apr-26 A	0.00	0.00	0.00	100%	100%	HDPE ducts	
DAM3-E-MS-E-0260	Main program system & controller	2	06-Apr-26	07-Apr-26	30-Apr-26 A	30-Apr-26 A	0.00	0.00	0.00	100%	100%	Main program	
DAM3-E-MS-E-0270	PLC controller	2	08-Apr-26	09-Apr-26	30-Apr-26 A	30-Apr-26 A	0.00	0.00	0.00	100%	100%	PLC controller	
EXTERNAL		14	30-Mar-26	14-Apr-26	11-Jun-26 A	11-Jun-26 A	0.00	0.00	0.00	0%	0%	11-Jun-26 A,	
DAM3-E-MS-EX-0010	Asphalt works	2	30-Mar-26	31-Mar-26	11-Jun-26 A	11-Jun-26 A	0.00	0.00	0.00	100%	100%	Asphalt work	
DAM3-E-MS-EX-0020	Concrete parking bumper	2	01-Apr-26	02-Apr-26	11-Jun-26 A	11-Jun-26 A	0.00	0.00	0.00	100%	100%	Concrete par	
DAM3-E-MS-EX-0030	Road markings	2	04-Apr-26	05-Apr-26	11-Jun-26 A	11-Jun-26 A	0.00	0.00	0.00	100%	100%	Road markin	
DAM3-E-MS-EX-0040	Road signs	2	06-Apr-26	07-Apr-26	11-Jun-26 A	11-Jun-26 A	0.00	0.00	0.00	100%	100%	Road signs	
DAM3-E-MS-EX-0060	Interlock tiles	2	08-Apr-26	09-Apr-26	11-Jun-26 A	11-Jun-26 A	0.00	0.00	0.00	100%	100%	Interlock tiles	
DAM3-E-MS-EX-0070	Curbstones	2	11-Apr-26	12-Apr-26	11-Jun-26 A	11-Jun-26 A	0.00	0.00	0.00	100%	100%	Curbstones	
DAM3-E-MS-EX-0080	Gravel bedding	2	13-Apr-26	14-Apr-26	11-Jun-26 A	11-Jun-26 A	0.00	0.00	0.00	100%	100%	Gravel beddi	
ENVIRONMETAL		55	03-Feb-26	23-Feb-26	08-Feb-26 A	18-Feb-26 A	0.00	0.00	0.00	0%	0%	18-Feb-26 A, EN	
DAM3-E-MS-EN-0010	HDPE pipes for fire system	2	03-Feb-26	04-Feb-26	08-Feb-26 A	08-Feb-26 A	0.00	0.00	0.00	100%	100%	HDPE pipes for	
DAM3-E-MS-EN-0030	HDPE pipes for water supply system	2	08-Feb-26	09-Feb-26	08-Feb-26 A	08-Feb-26 A	0.00	0.00	0.00	100%	100%	HDPE pipes for	
DAM3-E-MS-EN-0080	UPVC pipes	2	19-Feb-26	23-Feb-26	08-Feb-26 A	08-Feb-26 A	0.00	0.00	0.00	100%	100%	UPVC pipes	
DAM3-E-MS-EN-0020	Directly buried gate valve for fire system	2	05-Feb-26	07-Feb-26	16-Feb-26 A	16-Feb-26 A	0.00	0.00	0.00	100%	100%	Directly buried ga	
DAM3-E-MS-EN-0040	Directly buried gate valve for water system	2	10-Feb-26	11-Feb-26	16-Feb-26 A	16-Feb-26 A	0.00	0.00	0.00	100%	100%	Directly buried ga	

Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary

Date	Revision	Checked	Approved
06-Oct-26	Weekly Report		

Activity ID	Activity Name	Original Duration	BL Project Start	BL Project Finish	Start	Finish	Budgeted Total Cost	Planned Value Cost	Earned Value Cost	Schedule % Complete	Performance % Complete
DAM3-E-MS-EN-0050	Air valve	2	12-Feb-26	14-Feb-26	18-Feb-26 A	18-Feb-26 A	0.00	0.00	0.00	100%	100%
DAM3-E-MS-EN-0060	Washout valve	2	15-Feb-26	16-Feb-26	18-Feb-26 A	18-Feb-26 A	0.00	0.00	0.00	100%	100%
DAM3-E-MS-EN-0070	Gate valve	2	17-Feb-26	19-Feb-26	18-Feb-26 A	18-Feb-26 A	0.00	0.00	0.00	100%	100%
REVIEW AND APPROVAL		104	29-Jan-26	20-Apr-26	20-Jan-26 A	14-Jun-26 A	2,879,895.75	2,879,895.75	2,879,895.75	100%	100%
STRUCTURAL		20	29-Jan-26	12-Feb-26	20-Jan-26 A	07-Apr-26 A	481,112.68	481,112.68	481,112.68	100%	100%
DAM3-E-MA-C-0020	Concrete mix	5	01-Feb-26	05-Feb-26	20-Jan-26 A	20-Jan-26 A	251,751.70	251,751.70	251,751.70	100%	100%
DAM3-E-MA-C-0030	Polyethylene sheet	5	03-Feb-26	08-Feb-26	22-Jan-26 A	29-Jan-26 A	13,035.98	13,035.98	13,035.98	100%	100%
DAM3-E-MA-C-0040	Bitumen paint	5	05-Feb-26	10-Feb-26	22-Jan-26 A	29-Jan-26 A	28,944.10	28,944.10	28,944.10	100%	100%
DAM3-E-MA-C-0050	Rebar	5	08-Feb-26	12-Feb-26	22-Jan-26 A	29-Jan-26 A	167,834.46	167,834.46	167,834.46	100%	100%
DAM3-E-MA-C-0010	Anti termite	5	29-Jan-26	03-Feb-26	14-Mar-26 A	07-Apr-26 A	19,546.44	19,546.44	19,546.44	100%	100%
ARCHITECTURAL		93	03-Feb-26	12-Mar-26	07-Feb-26 A	14-Jun-26 A	1,232,403.28	1,232,403.28	1,232,403.28	100%	100%
DAM3-E-MA-A-0030	Steel ladder	5	05-Feb-26	10-Feb-26	07-Feb-26 A	10-Feb-26 A	4,846.16	4,846.16	4,846.16	100%	100%
DAM3-E-MA-A-1700	PES -Steel Structure	5	12-Feb-26	17-Feb-26	07-Feb-26 A	17-Mar-26 A	799,834.94	799,834.94	799,834.94	100%	100%
DAM3-E-MA-A-0100	Doors	5	12-Feb-26	17-Feb-26	19-Feb-26 A	25-Feb-26 A	75,386.56	75,386.56	75,386.56	100%	100%
DAM3-E-MA-A-0110	Windows	5	15-Feb-26	21-Feb-26	19-Feb-26 A	25-Feb-26 A	52,525.19	52,525.19	52,525.19	100%	100%
DAM3-E-MA-A-0160	Interni paint	5	25-Feb-26	03-Mar-26	29-Mar-26 A	03-May-26 A	21,754.04	21,754.04	21,754.04	100%	100%
DAM3-E-MA-A-0120	Ceramic tiles	5	17-Feb-26	24-Feb-26	30-Mar-26 A	04-May-26 A	36,151.26	36,151.26	36,151.26	100%	100%
DAM3-E-MA-A-0170	Gypsum board	5	01-Mar-26	05-Mar-26	19-Apr-26 A	14-Jun-26 A	23,046.95	23,046.95	23,046.95	100%	100%
DAM3-E-MA-A-0150	Epoxy paint	5	23-Feb-26	01-Mar-26	21-Apr-26 A	26-Apr-26 A	56,848.54	56,848.54	56,848.54	100%	100%
DAM3-E-MA-A-1720	Aluminum Composite Panel	5	03-Mar-26	08-Mar-26	21-Apr-26 A	26-Apr-26 A	86,631.78	86,631.78	86,631.78	100%	100%
DAM3-E-MA-A-0020	Concrete masonry unit (CMU)	5	03-Feb-26	08-Feb-26	26-Apr-26 A	29-Apr-26 A	62,820.36	62,820.36	62,820.36	100%	100%
DAM3-E-MA-A-0130	Granite strip	5	19-Feb-26	26-Feb-26	09-May-26 A	17-May-26 A	330.55	330.55	330.55	100%	100%
DAM3-E-MA-A-0040	Steel gratings	5	08-Feb-26	12-Feb-26	21-May-26 A	24-May-26 A	3,179.40	3,179.40	3,179.40	100%	100%
DAM3-E-MA-A-1750	Steel fence and gates	5	05-Mar-26	10-Mar-26	23-May-26 A	25-May-26 A	3,548.60	3,548.60	3,548.60	100%	100%
DAM3-E-MA-A-1760	Identification sign; ID01 & ID02	5	08-Mar-26	12-Mar-26	08-Jun-26 A	13-Jun-26 A	4,743.41	4,743.41	4,743.41	100%	100%
DAM3-E-MA-A-0050	Steel rails	5	10-Feb-26	15-Feb-26	13-Jun-26 A	14-Jun-26 A	755.54	755.54	755.54	100%	100%
MECHANICAL		101	03-Feb-26	20-Apr-26	05-Feb-26 A	14-Jun-26 A	303,435.06	303,435.06	303,435.06	100%	100%
DAM3-E-MA-M-0080	PPR pipes	5	05-Feb-26	10-Feb-26	05-Feb-26 A	11-May-26 A	11,485.19	11,485.19	11,485.19	100%	100%
DAM3-E-MA-M-0250	Fire pumps	5	04-Apr-26	08-Apr-26	05-Feb-26 A	24-Feb-26 A	15,505.34	15,505.34	15,505.34	100%	100%
DAM3-E-MA-M-0310	Booster pump	5	08-Apr-26	13-Apr-26	05-Feb-26 A	11-Feb-26 A	1,938.67	1,938.67	1,938.67	100%	100%
DAM3-E-MA-M-0010	U/G HDPE pipes	5	15-Feb-26	21-Feb-26	07-Feb-26 A	08-Mar-26 A	7,495.73	7,495.73	7,495.73	100%	100%
DAM3-E-MA-M-0030	Fire hose cabinet	5	17-Feb-26	24-Feb-26	07-Feb-26 A	01-Mar-26 A	7,466.16	7,466.16	7,466.16	100%	100%
DAM3-E-MA-M-0110	UPVC pipes	5	05-Mar-26	10-Mar-26	07-Feb-26 A	12-Apr-26 A	19,003.97	19,003.97	19,003.97	100%	100%
DAM3-E-MA-M-0150	Electric water heater	5	15-Mar-26	23-Mar-26	08-Feb-26 A	01-Mar-26 A	896.17	896.17	896.17	100%	100%
DAM3-E-MA-M-0160	Western water closet	5	21-Mar-26	25-Mar-26	08-Feb-26 A	17-May-26 A	9,812.19	9,812.19	9,812.19	100%	100%
DAM3-E-MA-M-0190	Lavatory / wash basin	5	28-Mar-26	01-Apr-26	08-Feb-26 A	17-May-26 A	10,548.52	10,548.52	10,548.52	100%	100%
DAM3-E-MA-M-0140	Gully trap	5	12-Mar-26	21-Mar-26	09-Feb-26 A	26-Feb-26 A	2,397.38	2,397.38	2,397.38	100%	100%
DAM3-E-MA-M-0180	Toilet Fittings	5	25-Mar-26	30-Mar-26	09-Feb-26 A	01-Jun-26 A	11,319.13	11,319.13	11,319.13	100%	100%
DAM3-E-MA-M-0020	Seamless black steel or ERW pipes	5	03-Feb-26	08-Feb-26	10-Feb-26 A	26-Feb-26 A	35,657.12	35,657.12	35,657.12	100%	100%
DAM3-E-MA-M-0040	Automatic air release valve	5	19-Feb-26	26-Feb-26	10-Feb-26 A	26-Feb-26 A	265.43	265.43	265.43	100%	100%
DAM3-E-MA-M-0050	OS & Y gate valve	5	23-Feb-26	01-Mar-26	10-Feb-26 A	26-Feb-26 A	1,744.73	1,744.73	1,744.73	100%	100%
DAM3-E-MA-M-0060	Fire alarm check valve	5	25-Feb-26	03-Mar-26	10-Feb-26 A	26-Feb-26 A	3,998.51	3,998.51	3,998.51	100%	100%
DAM3-E-MA-M-0270	Fire fighting valves	5	06-Apr-26	11-Apr-26	10-Feb-26 A	26-Mar-26 A	1,332.84	1,332.84	1,332.84	100%	100%
DAM3-E-MA-M-0330	Water supply valves	5	13-Apr-26	18-Apr-26	10-Feb-26 A	26-Mar-26 A	467.18	467.18	467.18	100%	100%
DAM3-E-MA-M-0090	Ball valve	5	01-Mar-26	05-Mar-26	14-Feb-26 A	16-Apr-26 A	2,134.82	2,134.82	2,134.82	100%	100%
DAM3-E-MA-M-0170	Bib tap	5	23-Mar-26	28-Mar-26	14-Feb-26 A	16-Apr-26 A	936.14	936.14	936.14	100%	100%
DAM3-E-MA-M-3410	Water tap	5	15-Apr-26	20-Apr-26	14-Feb-26 A	16-Apr-26 A	1,415.62	1,415.62	1,415.62	100%	100%
DAM3-E-MA-M-0120	Roof vent caps	5	08-Mar-26	12-Mar-26	16-Feb-26 A	14-Jun-26 A	456.64	456.64	456.64	100%	100%
DAM3-E-MA-M-0130	Floor drain	5	10-Mar-26	15-Mar-26	16-Feb-26 A	04-Jun-26 A	11,113.99	11,113.99	11,113.99	100%	100%



Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary

Date	Revision	Checked	Approved
06-Oct-26	Weekly Report		

Activity ID	Activity Name	Original Duration	BL Project Start	BL Project Finish	Start	Finish	Budgeted Total Cost	Planned Value Cost	Earned Value Cost	Schedule % Complete	Performance % Complete
DAM3-E-MA-M-0340	Warning tapes	5	15-Feb-26	21-Feb-26	16-Feb-26 A	03-Mar-26 A	2,111.55	2,111.55	2,111.55	100%	100%
DAM3-E-MA-M-0320	GRP tank	5	11-Apr-26	15-Apr-26	02-Mar-26 A	07-Apr-26 A	31,477.96	31,477.96	31,477.96	100%	100%
DAM3-E-MA-M-0220	HVAC duct	5	08-Feb-26	12-Feb-26	04-Mar-26 A	12-May-26 A	73,629.07	73,629.07	73,629.07	100%	100%
DAM3-E-MA-M-0230	Flexible duct	5	10-Feb-26	15-Feb-26	04-Mar-26 A	12-May-26 A	10,444.45	10,444.45	10,444.45	100%	100%
DAM3-E-MA-M-0200	Inline exhaust fans	5	30-Mar-26	04-Apr-26	18-Mar-26 A	19-Apr-26 A	4,121.24	4,121.24	4,121.24	100%	100%
DAM3-E-MA-M-0210	Wall propeller type exhaust fans	5	01-Apr-26	06-Apr-26	18-Mar-26 A	19-Apr-26 A	23,066.33	23,066.33	23,066.33	100%	100%
DAM3-E-MA-M-0240	Exhaust diffuser	5	12-Feb-26	17-Feb-26	01-Jun-26 A	04-Jun-26 A	1,056.00	1,056.00	1,056.00	100%	100%
DAM3-E-MA-M-0100	Capped connection	5	03-Mar-26	08-Mar-26	13-Jun-26 A	14-Jun-26 A	136.99	136.99	136.99	100%	100%
ELECTRICAL		74	05-Feb-26	15-Apr-26	09-Feb-26 A	14-Jun-26 A	472,829.48	472,829.48	472,829.48	100%	100%
DAM3-E-MA-E-0040	PVC conduits	5	05-Feb-26	10-Feb-26	09-Feb-26 A	01-Mar-26 A	2,360.80	2,360.80	2,360.80	100%	100%
DAM3-E-MA-E-0130	Fire alarm system	5	23-Mar-26	28-Mar-26	11-Feb-26 A	30-Mar-26 A	41,920.11	41,920.11	41,920.11	100%	100%
DAM3-E-MA-E-0240	Access control system	5	04-Apr-26	08-Apr-26	11-Feb-26 A	07-Mar-26 A	13,602.34	13,602.34	13,602.34	100%	100%
DAM3-E-MA-E-0060	Suspended High Bay LED lights	5	05-Mar-26	10-Mar-26	03-Mar-26 A	07-Mar-26 A	14,938.02	14,938.02	14,938.02	100%	100%
DAM3-E-MA-E-0070	Flood lights	5	08-Mar-26	12-Mar-26	03-Mar-26 A	07-Mar-26 A	2,268.18	2,268.18	2,268.18	100%	100%
DAM3-E-MA-E-0080	Recessed mounted LED downlight	5	10-Mar-26	15-Mar-26	03-Mar-26 A	07-Mar-26 A	20,081.13	20,081.13	20,081.13	100%	100%
DAM3-E-MA-E-0090	LED Emergency Lights wall mounted	5	12-Mar-26	21-Mar-26	03-Mar-26 A	07-Mar-26 A	4,144.06	4,144.06	4,144.06	100%	100%
DAM3-E-MA-E-0100	LED Emergency Exit Light	5	15-Mar-26	23-Mar-26	03-Mar-26 A	07-Mar-26 A	1,145.13	1,145.13	1,145.13	100%	100%
DAM3-E-MA-E-0190	Surface mounted lights	5	30-Mar-26	04-Apr-26	03-Mar-26 A	07-Mar-26 A	11,068.82	11,068.82	11,068.82	100%	100%
DAM3-E-MA-E-0250	Solar system	4	06-Apr-26	11-Apr-26	03-Mar-26 A	25-Apr-26 A	124,744.29	124,744.29	124,744.29	100%	100%
DAM3-E-MA-E-0170	Street Lighting poles	4	25-Mar-26	30-Mar-26	04-Mar-26 A	20-May-26 A	10,525.31	10,525.31	10,525.31	100%	100%
DAM3-E-MA-E-0140	Wiring devices	5	15-Feb-26	21-Feb-26	07-Mar-26 A	08-Mar-26 A	9,962.15	9,962.15	9,962.15	100%	100%
DAM3-E-MA-E-210	Cable Tray	5	10-Feb-26	15-Feb-26	07-Mar-26 A	08-Mar-26 A	159.57	159.57	159.57	100%	100%
DAM3-E-MA-E-0010	Low Voltage cables	5	19-Feb-26	26-Feb-26	16-Mar-26 A	29-Mar-26 A	44,855.17	44,855.17	44,855.17	100%	100%
DAM3-E-MA-E-0050	Wires	5	08-Feb-26	12-Feb-26	16-Mar-26 A	29-Mar-26 A	1,106.91	1,106.91	1,106.91	100%	100%
DAM3-E-MA-E-0120	Grounding system	5	12-Feb-26	17-Feb-26	16-Mar-26 A	29-Mar-26 A	9,771.19	9,771.19	9,771.19	100%	100%
DAM3-E-MA-E-0230	CCTV System	4	01-Apr-26	06-Apr-26	28-Mar-26 A	13-Apr-26 A	37,604.85	37,604.85	37,604.85	100%	100%
DAM3-E-MA-E-0030	Disconnect switches	5	03-Mar-26	08-Mar-26	29-Mar-26 A	14-Jun-26 A	15,086.41	15,086.41	15,086.41	100%	100%
DAM3-E-MA-E-0110	Wall mounted, duplex, telephone and data outlet	4	21-Mar-26	25-Mar-26	29-Mar-26 A	13-Apr-26 A	13,294.12	13,294.12	13,294.12	100%	100%
DAM3-E-MA-E-0020	Main distribution board (MDB)	5	23-Feb-26	01-Mar-26	26-Apr-26 A	12-May-26 A	15,994.03	15,994.03	15,994.03	100%	100%
DAM3-E-MA-E-0180	Distribution board for pump room	4	28-Mar-26	01-Apr-26	26-Apr-26 A	12-May-26 A	11,002.71	11,002.71	11,002.71	100%	100%
DAM3-E-MA-E-190	Lighting panel board	5	25-Feb-26	03-Mar-26	26-Apr-26 A	12-May-26 A	9,064.43	9,064.43	9,064.43	100%	100%
DAM3-E-MA-E-200	PP-AC panel	5	01-Mar-26	05-Mar-26	26-Apr-26 A	12-May-26 A	10,662.68	10,662.68	10,662.68	100%	100%
DAM3-E-MA-E-0160	HDPE ducts	5	17-Feb-26	24-Feb-26	30-Apr-26 A	03-May-26 A	26,402.96	26,402.96	26,402.96	100%	100%
DAM3-E-MA-E-0260	Main program system & controller	5	08-Apr-26	13-Apr-26	30-Apr-26 A	12-May-26 A	12,578.11	12,578.11	12,578.11	100%	100%
DAM3-E-MA-E-0270	PLC controller	5	11-Apr-26	15-Apr-26	30-Apr-26 A	12-May-26 A	8,486.00	8,486.00	8,486.00	100%	100%
EXTERNAL		29	01-Apr-26	20-Apr-26	11-Jun-26 A	13-Jun-26 A	332,383.67	332,383.67	332,383.67	100%	100%
DAM3-E-MA-EX-0010	Asphalt works	5	01-Apr-26	06-Apr-26	11-Jun-26 A	13-Jun-26 A	280,347.76	280,347.76	280,347.76	100%	100%
DAM3-E-MA-EX-0020	Concrete parking bumper	5	04-Apr-26	08-Apr-26	11-Jun-26 A	13-Jun-26 A	1,433.72	1,433.72	1,433.72	100%	100%
DAM3-E-MA-EX-0030	Road markings	5	06-Apr-26	11-Apr-26	11-Jun-26 A	13-Jun-26 A	1,696.34	1,696.34	1,696.34	100%	100%
DAM3-E-MA-EX-0040	Road signs	5	08-Apr-26	13-Apr-26	11-Jun-26 A	13-Jun-26 A	4,654.29	4,654.29	4,654.29	100%	100%
DAM3-E-MA-EX-0060	Interlock tiles	5	11-Apr-26	15-Apr-26	11-Jun-26 A	13-Jun-26 A	21,297.02	21,297.02	21,297.02	100%	100%
DAM3-E-MA-EX-0070	Curbstones	5	13-Apr-26	18-Apr-26	11-Jun-26 A	13-Jun-26 A	13,036.86	13,036.86	13,036.86	100%	100%
DAM3-E-MA-EX-0080	Gravel bedding	5	15-Apr-26	20-Apr-26	11-Jun-26 A	13-Jun-26 A	9,917.68	9,917.68	9,917.68	100%	100%
ENVIRONMETAL		59	05-Feb-26	01-Mar-26	08-Feb-26 A	14-Jun-26 A	57,731.58	57,731.58	57,731.58	100%	100%
DAM3-E-MA-EN-0010	HDPE pipes for fire system	5	05-Feb-26	10-Feb-26	08-Feb-26 A	26-Feb-26 A	21,745.93	21,745.93	21,745.93	100%	100%
DAM3-E-MA-EN-0030	HDPE pipes for water supply system	5	10-Feb-26	15-Feb-26	08-Feb-26 A	26-Feb-26 A	1,598.26	1,598.26	1,598.26	100%	100%
DAM3-E-MA-EN-0080	UPVC pipes	5	23-Feb-26	01-Mar-26	08-Feb-26 A	26-Feb-26 A	20,218.26	20,218.26	20,218.26	100%	100%
DAM3-E-MA-EN-0020	Directly buried gate valve for fire system	5	08-Feb-26	12-Feb-26	16-Feb-26 A	25-May-26 A	1,090.50	1,090.50	1,090.50	100%	100%
DAM3-E-MA-EN-0040	Directly buried gate valve for water system	5	12-Feb-26	17-Feb-26	16-Feb-26 A	25-May-26 A	2,414.78	2,414.78	2,414.78	100%	100%

2026 2027

Warning tapes
GRP tank
HVAC duct
Flexible duct
Inline exhaust
Wall propeller
Exhaust diffu
Capped con
14-Jun-26 A,
PVC conduits
Fire alarm syste
Access control s
Suspended Hig
Flood lights
Recessed moun
LED Emergency
LED Emergency
Surface mounte
Solar system
Street Lightin
Wiring devices
Cable Tray
Low Voltage ca
Wires
Grounding syst
CCTV System
Disconnect s
Wall mounted,
Main distributi
Distribution bo
Lighting pane
PP-AC panel
HDPE ducts
Main program
PLC controlle
13-Jun-26 A,
Asphalt work
Concrete pa
Road markin
Road signs
Interlock tiles
Curbstones
Gravel beddi
14-Jun-26 A,
HDPE pipes for
HDPE pipes for
UPVC pipes
Directly buried
Directly buried

Activity ID	Activity Name	Original Duration	BL Project Start	BL Project Finish	Start	Finish	Budgeted Total Cost	Planned Value Cost	Earned Value Cost	Schedule % Complete	Performance % Complete
DAM3-E-MA-EN-0050	Air valve	5	15-Feb-26	21-Feb-26	18-Feb-26 A	26-Feb-26 A	1,963.06	1,963.06	1,963.06	100%	100%
DAM3-E-MA-EN-0060	Washout valve	5	17-Feb-26	24-Feb-26	18-Feb-26 A	14-Jun-26 A	2,302.04	2,302.04	2,302.04	100%	100%
DAM3-E-MA-EN-0070	Gate valve	5	19-Feb-26	26-Feb-26	18-Feb-26 A	14-Jun-26 A	6,398.75	6,398.75	6,398.75	100%	100%
METHOD STATEMENTS		125	29-Jan-26	23-Apr-26	07-Feb-26 A	23-Jun-26 A	0.00	0.00	0.00	0%	0%
PREPARATION AND SUBMITTAL		112	29-Jan-26	25-Mar-26	07-Feb-26 A	22-Jun-26 A	0.00	0.00	0.00	0%	0%
DAM3-E-MT-C-0010	Method Statement for Structural Works	7	29-Jan-26	05-Feb-26	07-Feb-26 A	22-Jun-26 A	0.00	0.00	0.00	100%	100%
DAM3-E-MT-A-0020	Method Statement for Architectural Works	7	07-Feb-26	14-Feb-26	05-Mar-26 A	22-Jun-26 A	0.00	0.00	0.00	100%	100%
DAM3-E-MT-M-0030	Method Statement for Mechanical Works	7	15-Feb-26	24-Feb-26	10-May-26 A	22-Jun-26 A	0.00	0.00	0.00	100%	100%
DAM3-E-MT-E-0040	Method Statement for Electrical Works	7	24-Feb-26	04-Mar-26	10-May-26 A	22-Jun-26 A	0.00	0.00	0.00	100%	100%
DAM3-E-MT-EX-0050	Method Statement for External Works	7	05-Mar-26	12-Mar-26	21-Jun-26 A	22-Jun-26 A	0.00	0.00	0.00	100%	100%
DAM3-E-MT-ENV-0060	Method Statement for Environmental Works	8	14-Mar-26	25-Mar-26	21-Jun-26 A	22-Jun-26 A	0.00	0.00	0.00	100%	100%
REVIEW AND APPROVAL		51	07-Feb-26	22-Apr-26	07-Feb-26 A	23-Jun-26 A	0.00	0.00	0.00	0%	0%
DAM3-E-MT-C-1010	Method Statement for Structural Works	10	07-Feb-26	17-Feb-26	07-Feb-26 A	23-Jun-26 A	0.00	0.00	0.00	100%	100%
DAM3-E-MT-A-1020	Method Statement for Architectural Works	10	18-Feb-26	03-Mar-26	05-Mar-26 A	23-Jun-26 A	0.00	0.00	0.00	100%	100%
DAM3-E-MT-M-1030	Method Statement for Mechanical Works	10	04-Mar-26	15-Mar-26	10-May-26 A	23-Jun-26 A	0.00	0.00	0.00	100%	100%
DAM3-E-MT-E-1040	Method Statement for Electrical Works	10	16-Mar-26	30-Mar-26	10-May-26 A	23-Jun-26 A	0.00	0.00	0.00	100%	100%
DAM3-E-MT-EX-1050	Method Statement for External Works	10	31-Mar-26	11-Apr-26	21-Jun-26 A	23-Jun-26 A	0.00	0.00	0.00	100%	100%
DAM3-E-MT-ENV-1060	Method Statement for Environmental Works	10	12-Apr-26	22-Apr-26	21-Jun-26 A	23-Jun-26 A	0.00	0.00	0.00	100%	100%
STAGING		42	18-Feb-26	23-Apr-26	09-Feb-26 A	23-Jun-26 A	0.00	0.00	0.00	0%	0%
DAM3-E-MT-C-2010	Method Statement for Structural Works	1	18-Feb-26	19-Feb-26	09-Feb-26 A	23-Jun-26 A	0.00	0.00	0.00	100%	100%
DAM3-E-MT-M-2030	Method Statement for Mechanical Works	1	16-Mar-26	16-Mar-26	10-May-26 A	23-Jun-26 A	0.00	0.00	0.00	100%	100%
DAM3-E-MT-E-2040	Method Statement for Electrical Works	1	31-Mar-26	31-Mar-26	10-May-26 A	23-Jun-26 A	0.00	0.00	0.00	100%	100%
DAM3-E-MT-A-2020	Method Statement for Architectural Works	4	04-Mar-26	08-Mar-26	21-Jun-26 A	23-Jun-26 A	0.00	0.00	0.00	100%	100%
DAM3-E-MT-EX-2050	Method Statement for External Works	1	12-Apr-26	12-Apr-26	21-Jun-26 A	23-Jun-26 A	0.00	0.00	0.00	100%	100%
DAM3-E-MT-ENV-2060	Method Statement for Environmental Works	1	23-Apr-26	23-Apr-26	21-Jun-26 A	23-Jun-26 A	0.00	0.00	0.00	100%	100%
PROCUREMENT (20%)		258	04-Feb-26	15-Nov-26	14-Jan-26 A	27-Sep-26 A	19,199,305.00	18,012,864.10	19,199,305.00	93.82%	100%
LONG LEAD MATERIALS		245	09-Feb-26	15-Nov-26	14-Jan-26 A	27-Sep-26 A	9,350,010.31	8,167,494.39	9,350,010.31	87.35%	100%
ARCHITECTURAL		145	18-Feb-26	06-Jul-26	14-Jan-26 A	20-Aug-26 A	6,184,977.93	6,184,977.93	6,184,977.93	100%	100%
PO ISSUE		90	18-Feb-26	28-Feb-26	14-Jan-26 A	22-Mar-26 A	0.00	0.00	0.00	0%	0%
DAM3-E-PO-A-1700	PES -Steel Structure	5	18-Feb-26	25-Feb-26	14-Jan-26 A	14-Jan-26 A	0.00	0.00	0.00	100%	100%
DAM3-P-PO-A-180	Doors	5	18-Feb-26	25-Feb-26	18-Mar-26 A	18-Mar-26 A	0.00	0.00	0.00	100%	100%
DAM3-P-PO-A-190	Windows	5	21-Feb-26	28-Feb-26	22-Mar-26 A	22-Mar-26 A	0.00	0.00	0.00	100%	100%
MANUFACTURING		99	25-Feb-26	20-Jun-26	14-Jan-26 A	23-Jun-26 A	0.00	0.00	0.00	0%	0%
DAM3-E-MF-A-1700	PES -Steel Structure	45	25-Feb-26	22-Apr-26	14-Jan-26 A	25-May-26 A	0.00	0.00	0.00	100%	100%
DAM3-P-MF-A-180	Doors	90	25-Feb-26	17-Jun-26	21-Mar-26 A	23-Jun-26 A	0.00	0.00	0.00	100%	100%
DAM3-P-MF-A-190	Windows	90	01-Mar-26	20-Jun-26	25-Mar-26 A	23-Jun-26 A	0.00	0.00	0.00	100%	100%
DELIVERY TO SITE		59	23-Apr-26	04-Jul-26	31-May-26 A	20-Aug-26 A	6,184,977.93	6,184,977.93	6,184,977.93	100%	100%
DAM3-P-DL-A-1700	PES -Steel Structure -1	7	23-Apr-26	30-Apr-26	31-May-26 A	31-May-26 A	2,369,269.97	2,369,269.97	2,369,269.97	100%	100%
DAM3-P-DL-A-1770	PES -Steel Structure -2	7	02-May-26	09-May-26	10-Jun-26 A	14-Jun-26 A	740,740.74	740,740.74	740,740.74	100%	100%
DAM3-P-DL-A-1780	PES -Steel Structure -3	7	18-Jun-26	25-Jun-26	14-Jun-26 A	14-Jul-26 A	740,740.74	740,740.74	740,740.74	100%	100%
DAM3-P-DL-A-1790	PES -Steel Structure -4	7	27-Jun-26	04-Jul-26	01-Jul-26 A	01-Jul-26 A	1,481,481.48	1,481,481.48	1,481,481.48	100%	100%
DAM3-P-DL-A-180	Doors	7	18-Jun-26	25-Jun-26	18-Aug-26 A	20-Aug-26 A	502,577.07	502,577.07	502,577.07	100%	100%
DAM3-P-DL-A-190	Windows	7	21-Jun-26	28-Jun-26	19-Aug-26 A	20-Aug-26 A	350,167.93	350,167.93	350,167.93	100%	100%
STAGING TIME		38	02-May-26	06-Jul-26	21-Jul-26 A	20-Aug-26 A	0.00	0.00	0.00	0%	0%
DAM3-E-ST-A-1700	PES -Steel Structure	2	02-May-26	03-May-26	21-Jul-26 A	22-Jul-26 A	0.00	0.00	0.00	100%	100%
DAM3-P-ST-A-180	Doors	7	27-Jun-26	04-Jul-26	18-Aug-26 A	20-Aug-26 A	0.00	0.00	0.00	100%	100%
DAM3-P-ST-A-190	Windows	7	29-Jun-26	06-Jul-26	19-Aug-26 A	20-Aug-26 A	0.00	0.00	0.00	100%	100%
ELECTRICAL		187	01-Mar-26	15-Nov-26	24-Mar-26 A	27-Sep-26 A	2,332,207.26	1,149,691.34	2,332,207.26	49.3%	100%
PO ISSUE		60	01-Mar-26	14-May-26	24-Mar-26 A	24-Mar-26 A	0.00	0.00	0.00	0%	0%

Activity ID	Activity Name	Original Duration	BL Project Start	BL Project Finish	Start	Finish	Budgeted Total Cost	Planned Value Cost	Earned Value Cost	Schedule % Complete	Performance % Complete	2026 2027
DAM3-P-PO-E-190	Main distribution board (MDB)	5	01-Mar-26	07-Mar-26	24-Mar-26 A	24-Mar-26 A	0.00	0.00	0.00	100%	100%	Main distributio
DAM3-P-PO-E-200	Suspended High Bay LED lights	5	24-Mar-26	29-Mar-26	24-Mar-26 A	24-Mar-26 A	0.00	0.00	0.00	100%	100%	Suspended Hig
DAM3-P-PO-E-210	Flood lights	5	30-Mar-26	04-Apr-26	24-Mar-26 A	24-Mar-26 A	0.00	0.00	0.00	100%	100%	Flood lights
DAM3-P-PO-E-220	Recessed mounted LED downlight	5	05-Apr-26	09-Apr-26	24-Mar-26 A	24-Mar-26 A	0.00	0.00	0.00	100%	100%	Recessed mou
DAM3-P-PO-E-230	LED Emergency Lights wall mounted	5	11-Apr-26	15-Apr-26	24-Mar-26 A	24-Mar-26 A	0.00	0.00	0.00	100%	100%	LED Emergenc
DAM3-P-PO-E-240	LED Emergency Exit Light	5	16-Apr-26	21-Apr-26	24-Mar-26 A	24-Mar-26 A	0.00	0.00	0.00	100%	100%	LED Emergenc
DAM3-P-PO-E-250	Fire alarm system	5	22-Apr-26	27-Apr-26	24-Mar-26 A	24-Mar-26 A	0.00	0.00	0.00	100%	100%	Fire alarm syste
DAM3-P-PO-E-260	Street Lighting poles	5	28-Apr-26	03-May-26	24-Mar-26 A	24-Mar-26 A	0.00	0.00	0.00	100%	100%	Street Lighting
DAM3-P-PO-E-270	Distribution board for pump room	5	04-May-26	09-May-26	24-Mar-26 A	24-Mar-26 A	0.00	0.00	0.00	100%	100%	Distribution boa
DAM3-P-PO-E-280	Surface mounted lights	5	10-May-26	14-May-26	24-Mar-26 A	24-Mar-26 A	0.00	0.00	0.00	100%	100%	Surface mounte
DAM3-E-PO-E-190	Lighting panel board	5	07-Mar-26	12-Mar-26	24-Mar-26 A	24-Mar-26 A	0.00	0.00	0.00	100%	100%	Lighting panel b
DAM3-E-PO-E-200	PP-AC panel	5	12-Mar-26	22-Mar-26	24-Mar-26 A	24-Mar-26 A	0.00	0.00	0.00	100%	100%	PP-AC panel
DAM3-E-PO-E-0230	CCTV System	5	07-Apr-26	12-Apr-26	24-Mar-26 A	24-Mar-26 A	0.00	0.00	0.00	100%	100%	CCTV System
DAM3-E-PO-E-0240	Access control system	5	09-Apr-26	14-Apr-26	24-Mar-26 A	24-Mar-26 A	0.00	0.00	0.00	100%	100%	Access control s
DAM3-E-PO-E-0250	Solar system	5	12-Apr-26	16-Apr-26	24-Mar-26 A	24-Mar-26 A	0.00	0.00	0.00	100%	100%	Solar system
DAM3-E-PO-E-0260	Main program system & controller	5	14-Apr-26	19-Apr-26	24-Mar-26 A	24-Mar-26 A	0.00	0.00	0.00	100%	100%	Main program s
DAM3-E-PO-E-0270	PLC controller	5	16-Apr-26	21-Apr-26	24-Mar-26 A	24-Mar-26 A	0.00	0.00	0.00	100%	100%	PLC controller
MANUFACTURING		187	07-Mar-26	29-Oct-26	01-Apr-26 A	27-Sep-26 A	0.00	0.00	0.00	0%	0%	27-Sep-2
DAM3-P-MF-E-190	Main distribution board (MDB)	90	07-Mar-26	27-Jun-26	01-Apr-26 A	22-Aug-26 A	0.00	0.00	0.00	100%	100%	Main distrib
DAM3-E-MF-E-190	Lighting panel board	90	12-Mar-26	02-Jul-26	07-Apr-26 A	20-Sep-26 A	0.00	0.00	0.00	100%	100%	Lighting p
DAM3-E-MF-E-200	PP-AC panel	90	22-Mar-26	08-Jul-26	13-Apr-26 A	20-Sep-26 A	0.00	0.00	0.00	100%	100%	PP-AC pa
DAM3-E-MF-E-0240	Access control system	150	15-Apr-26	11-Oct-26	16-Apr-26 A	20-Sep-26 A	0.00	0.00	0.00	96.67%	100%	Access co
DAM3-P-MF-E-200	Suspended High Bay LED lights	90	30-Mar-26	15-Jul-26	20-Apr-26 A	27-Aug-26 A	0.00	0.00	0.00	100%	100%	Suspende
DAM3-E-MF-E-0230	CCTV System	120	13-Apr-26	02-Sep-26	25-Apr-26 A	20-Sep-26 A	0.00	0.00	0.00	100%	100%	CCTV Sy
DAM3-E-MF-E-0250	Solar system	150	18-Apr-26	13-Oct-26	25-Apr-26 A	20-Sep-26 A	0.00	0.00	0.00	95.33%	100%	Solar syst
DAM3-P-MF-E-210	Flood lights	90	05-Apr-26	21-Jul-26	28-Apr-26 A	27-Sep-26 A	0.00	0.00	0.00	100%	100%	Flood ligh
DAM3-E-MF-E-0260	Main program system & controller	155	20-Apr-26	21-Oct-26	29-Apr-26 A	20-Sep-26 A	0.00	0.00	0.00	90.97%	100%	Main prog
DAM3-E-MF-E-0270	PLC controller	160	22-Apr-26	29-Oct-26	02-May-26 A	20-Sep-26 A	0.00	0.00	0.00	86.88%	100%	PLC cont
DAM3-P-MF-E-220	Recessed mounted LED downlight	90	11-Apr-26	27-Jul-26	04-May-26 A	27-Sep-26 A	0.00	0.00	0.00	100%	100%	Recessed
DAM3-P-MF-E-230	LED Emergency Lights wall mounted	90	16-Apr-26	02-Aug-26	10-May-26 A	27-Sep-26 A	0.00	0.00	0.00	100%	100%	LED Eme
DAM3-P-MF-E-240	LED Emergency Exit Light	90	22-Apr-26	08-Aug-26	16-May-26 A	27-Sep-26 A	0.00	0.00	0.00	100%	100%	LED Eme
DAM3-P-MF-E-250	Fire alarm system	130	28-Apr-26	30-Sep-26	21-May-26 A	20-Sep-26 A	0.00	0.00	0.00	100%	100%	Fire alarm
DAM3-P-MF-E-260	Street Lighting poles	90	04-May-26	19-Aug-26	31-May-26 A	21-Jun-26 A	0.00	0.00	0.00	100%	100%	Street Lightin
DAM3-P-MF-E-270	Distribution board for pump room	90	10-May-26	25-Aug-26	06-Jun-26 A	21-Jun-26 A	0.00	0.00	0.00	100%	100%	Distribution b
DAM3-P-MF-E-280	Surface mounted lights	90	16-May-26	31-Aug-26	11-Jun-26 A	21-Jun-26 A	0.00	0.00	0.00	100%	100%	Surface mou
DELIVERY TO SITE		33	27-Jun-26	07-Nov-26	24-Aug-26 A	21-Sep-26 A	2,332,207.26	1,149,691.34	2,332,207.26	49.3%	100%	21-Sep-26
DAM3-P-DL-E-190	Main distribution board (MDB)	7	27-Jun-26	05-Jul-26	24-Aug-26 A	24-Aug-26 A	106,626.87	106,626.87	106,626.87	100%	100%	Main distrit
DAM3-P-DL-E-200	Suspended High Bay LED lights	7	16-Jul-26	23-Jul-26	29-Aug-26 A	29-Aug-26 A	99,586.79	99,586.79	99,586.79	100%	100%	Suspende
DAM3-P-DL-E-210	Flood lights	7	22-Jul-26	29-Jul-26	29-Aug-26 A	29-Aug-26 A	15,121.21	15,121.21	15,121.21	100%	100%	Flood light
DAM3-P-DL-E-220	Recessed mounted LED downlight	7	28-Jul-26	04-Aug-26	29-Aug-26 A	29-Aug-26 A	133,874.22	133,874.22	133,874.22	100%	100%	Recessed
DAM3-P-DL-E-230	LED Emergency Lights wall mounted	7	03-Aug-26	10-Aug-26	29-Aug-26 A	29-Aug-26 A	27,627.07	27,627.07	27,627.07	100%	100%	LED Emer
DAM3-P-DL-E-240	LED Emergency Exit Light	7	09-Aug-26	16-Aug-26	29-Aug-26 A	29-Aug-26 A	7,634.17	7,634.17	7,634.17	100%	100%	LED Emer
DAM3-P-DL-E-280	Surface mounted lights	7	01-Sep-26	08-Sep-26	29-Aug-26 A	29-Aug-26 A	73,792.16	73,792.16	73,792.16	100%	100%	Surface m
DAM3-P-DL-E-1900	Lighting panel board	7	02-Jul-26	11-Jul-26	01-Sep-26 A	21-Sep-26 A	60,429.51	60,429.51	60,429.51	100%	100%	Lighting p
DAM3-P-DL-E-2000	PP-AC panel	7	08-Jul-26	16-Jul-26	01-Sep-26 A	21-Sep-26 A	71,084.56	71,084.56	71,084.56	100%	100%	PP-AC pa
DAM3-P-DL-E-250	Fire alarm system	7	01-Oct-26	08-Oct-26	02-Sep-26 A	21-Sep-26 A	279,467.41	159,695.66	279,467.41	57.14%	100%	Fire alarm
DAM3-P-DL-E-0230	CCTV System	7	03-Sep-26	10-Sep-26	06-Sep-26 A	21-Sep-26 A	250,698.98	250,698.98	250,698.98	100%	100%	CCTV Sy
DAM3-P-DL-E-0260	Main program system & controller	7	22-Oct-26	29-Oct-26	06-Sep-26 A	21-Sep-26 A	83,856.79	0.00	83,856.79	0%	100%	Main prog
DAM3-P-DL-E-0270	PLC controller	7	31-Oct-26	07-Nov-26	07-Sep-26 A	21-Sep-26 A	56,576.55	0.00	56,576.55	0%	100%	PLC cont


Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary

Date	Revision	Checked	Approved
06-Oct-26	Weekly Report		

Activity ID	Activity Name	Original Duration	BL Project Start	BL Project Finish	Start	Finish	Budgeted Total Cost	Planned Value Cost	Earned Value Cost	Schedule % Complete	Performance % Complete
DAM3-P-DL-E-0250	Solar system	7	14-Oct-26	21-Oct-26	09-Sep-26 A	21-Sep-26 A	831,628.60	0.00	831,628.60	0%	100%
DAM3-P-DL-E-0240	Access control system	7	12-Oct-26	19-Oct-26	19-Sep-26 A	21-Sep-26 A	90,682.24	0.00	90,682.24	0%	100%
DAM3-P-DL-E-260	Street Lighting poles	7	20-Aug-26	27-Aug-26	19-Sep-26 A	21-Sep-26 A	70,168.75	70,168.75	70,168.75	100%	100%
DAM3-P-DL-E-270	Distribution board for pump room	7	26-Aug-26	02-Sep-26	19-Sep-26 A	20-Sep-26 A	73,351.39	73,351.39	73,351.39	100%	100%
STAGING TIME		38	05-Jul-26	15-Nov-26	24-Aug-26 A	21-Sep-26 A	0.00	0.00	0.00	0%	0%
DAM3-P-ST-E-190	Main distribution board (MDB)	7	05-Jul-26	13-Jul-26	24-Aug-26 A	24-Aug-26 A	0.00	0.00	0.00	100%	100%
DAM3-P-ST-E-200	Suspended High Bay LED lights	7	25-Jul-26	01-Aug-26	29-Aug-26 A	29-Aug-26 A	0.00	0.00	0.00	100%	100%
DAM3-P-ST-E-210	Flood lights	7	30-Jul-26	06-Aug-26	29-Aug-26 A	29-Aug-26 A	0.00	0.00	0.00	100%	100%
DAM3-P-ST-E-220	Recessed mounted LED downlight	7	05-Aug-26	12-Aug-26	29-Aug-26 A	29-Aug-26 A	0.00	0.00	0.00	100%	100%
DAM3-P-ST-E-230	LED Emergency Lights wall mounted	7	11-Aug-26	18-Aug-26	29-Aug-26 A	29-Aug-26 A	0.00	0.00	0.00	100%	100%
DAM3-P-ST-E-240	LED Emergency Exit Light	7	17-Aug-26	24-Aug-26	29-Aug-26 A	29-Aug-26 A	0.00	0.00	0.00	100%	100%
DAM3-P-ST-E-280	Surface mounted lights	7	09-Sep-26	16-Sep-26	29-Aug-26 A	29-Aug-26 A	0.00	0.00	0.00	100%	100%
DAM3-E-ST-E-190	Lighting panel board	7	11-Jul-26	19-Jul-26	01-Sep-26 A	21-Sep-26 A	0.00	0.00	0.00	100%	100%
DAM3-E-ST-E-200	PP-AC panel	7	16-Jul-26	25-Jul-26	01-Sep-26 A	21-Sep-26 A	0.00	0.00	0.00	100%	100%
DAM3-P-ST-E-250	Fire alarm system	7	10-Oct-26	17-Oct-26	02-Sep-26 A	21-Sep-26 A	0.00	0.00	0.00	0%	100%
DAM3-E-ST-E-0230	CCTV System	7	12-Sep-26	19-Sep-26	06-Sep-26 A	21-Sep-26 A	0.00	0.00	0.00	100%	100%
DAM3-E-ST-E-0260	Main program system & controller	7	31-Oct-26	07-Nov-26	06-Sep-26 A	21-Sep-26 A	0.00	0.00	0.00	0%	100%
DAM3-E-ST-E-0270	PLC controller	7	08-Nov-26	15-Nov-26	07-Sep-26 A	21-Sep-26 A	0.00	0.00	0.00	0%	100%
DAM3-E-ST-E-0250	Solar system	7	22-Oct-26	29-Oct-26	09-Sep-26 A	21-Sep-26 A	0.00	0.00	0.00	0%	100%
DAM3-P-ST-E-260	Street Lighting poles	7	29-Aug-26	05-Sep-26	19-Sep-26 A	21-Sep-26 A	0.00	0.00	0.00	100%	100%
DAM3-P-ST-E-270	Distribution board for pump room	7	03-Sep-26	10-Sep-26	19-Sep-26 A	21-Sep-26 A	0.00	0.00	0.00	100%	100%
DAM3-E-ST-E-0240	Access control system	7	20-Oct-26	27-Oct-26	19-Sep-26 A	21-Sep-26 A	0.00	0.00	0.00	0%	100%
MECHANICAL		216	09-Feb-26	13-Oct-26	01-Mar-26 A	20-Sep-26 A	832,825.12	832,825.12	832,825.12	100%	100%
PO ISSUE		84	09-Feb-26	29-Apr-26	01-Mar-26 A	01-Mar-26 A	0.00	0.00	0.00	0%	0%
DAM3-P-PO-M-340	Seamless black steel or ERW pipes	5	09-Feb-26	14-Feb-26	01-Mar-26 A	01-Mar-26 A	0.00	0.00	0.00	100%	100%
DAM3-P-PO-M-350	Fire hose cabinet	5	24-Feb-26	02-Mar-26	01-Mar-26 A	01-Mar-26 A	0.00	0.00	0.00	100%	100%
DAM3-P-PO-M-360	Western water closet	5	25-Mar-26	31-Mar-26	01-Mar-26 A	01-Mar-26 A	0.00	0.00	0.00	100%	100%
DAM3-P-PO-M-370	Wall propeller type exhaust fans	5	06-Apr-26	12-Apr-26	01-Mar-26 A	01-Mar-26 A	0.00	0.00	0.00	100%	100%
DAM3-P-PO-M-380	Fire pumps	5	12-Apr-26	18-Apr-26	01-Mar-26 A	01-Mar-26 A	0.00	0.00	0.00	100%	100%
DAM3-P-PO-M-400	Booster pump	5	18-Apr-26	23-Apr-26	01-Mar-26 A	01-Mar-26 A	0.00	0.00	0.00	100%	100%
DAM3-P-PO-M-410	GRP tank	5	23-Apr-26	29-Apr-26	01-Mar-26 A	01-Mar-26 A	0.00	0.00	0.00	100%	100%
MANUFACTURING		211	15-Feb-26	27-Sep-26	02-Mar-26 A	19-Sep-26 A	0.00	0.00	0.00	0%	0%
DAM3-P-MF-M-340	Seamless black steel or ERW pipes	120	15-Feb-26	13-Jul-26	02-Mar-26 A	29-Jun-26 A	0.00	0.00	0.00	100%	100%
DAM3-P-MF-M-350	Fire hose cabinet	120	03-Mar-26	27-Jul-26	02-Mar-26 A	19-Sep-26 A	0.00	0.00	0.00	100%	100%
DAM3-P-MF-M-360	Western water closet	150	31-Mar-26	27-Sep-26	02-Mar-26 A	19-Sep-26 A	0.00	0.00	0.00	100%	100%
DAM3-P-MF-M-370	Wall propeller type exhaust fans	100	12-Apr-26	10-Aug-26	02-Mar-26 A	09-Aug-26 A	0.00	0.00	0.00	100%	100%
DAM3-P-MF-M-380	Fire pumps	120	18-Apr-26	08-Sep-26	02-Mar-26 A	17-Sep-26 A	0.00	0.00	0.00	100%	100%
DAM3-P-MF-M-400	Booster pump	110	23-Apr-26	02-Sep-26	02-Mar-26 A	06-Sep-26 A	0.00	0.00	0.00	100%	100%
DAM3-P-MF-M-410	GRP tank	100	29-Apr-26	27-Aug-26	02-Mar-26 A	25-Aug-26 A	0.00	0.00	0.00	100%	100%
DELIVERY TO SITE		72	14-Jul-26	05-Oct-26	01-Jul-26 A	20-Sep-26 A	832,825.12	832,825.12	832,825.12	100%	100%
DAM3-P-DL-M-340	Seamless black steel or ERW pipes	7	14-Jul-26	21-Jul-26	01-Jul-26 A	11-Aug-26 A	237,714.11	237,714.11	237,714.11	100%	100%
DAM3-P-DL-M-370	Wall propeller type exhaust fans	7	10-Aug-26	18-Aug-26	10-Aug-26 A	20-Sep-26 A	153,775.51	153,775.51	153,775.51	100%	100%
DAM3-P-DL-M-410	GRP tank	7	27-Aug-26	05-Sep-26	29-Aug-26 A	31-Aug-26 A	209,853.09	209,853.09	209,853.09	100%	100%
DAM3-P-DL-M-400	Booster pump	7	02-Sep-26	10-Sep-26	07-Sep-26 A	07-Sep-26 A	12,924.47	12,924.47	12,924.47	100%	100%
DAM3-P-DL-M-350	Fire hose cabinet	7	28-Jul-26	04-Aug-26	19-Sep-26 A	20-Sep-26 A	49,774.39	49,774.39	49,774.39	100%	100%
DAM3-P-DL-M-360	Western water closet	7	27-Sep-26	05-Oct-26	19-Sep-26 A	20-Sep-26 A	65,414.62	65,414.62	65,414.62	100%	100%
DAM3-P-DL-M-380	Fire pumps	7	08-Sep-26	16-Sep-26	20-Sep-26 A	20-Sep-26 A	103,368.93	103,368.93	103,368.93	100%	100%
STAGING TIME		86	22-Jul-26	13-Oct-26	01-Jul-26 A	20-Sep-26 A	0.00	0.00	0.00	0%	0%
DAM3-P-ST-M-340	Seamless black steel or ERW pipes	7	22-Jul-26	29-Jul-26	01-Jul-26 A	11-Aug-26 A	0.00	0.00	0.00	100%	100%

Activity ID	Activity Name	Original Duration	BL Project Start	BL Project Finish	Start	Finish	Budgeted Total Cost	Planned Value Cost	Earned Value Cost	Schedule % Complete	Performance % Complete
DAM3-P-ST-M-370	Wall propeller type exhaust fans	7	18-Aug-26	26-Aug-26	10-Aug-26 A	20-Sep-26 A	0.00	0.00	0.00	100%	100%
DAM3-P-ST-M-410	GRP tank	7	05-Sep-26	13-Sep-26	29-Aug-26 A	31-Aug-26 A	0.00	0.00	0.00	100%	100%
DAM3-P-ST-M-400	Booster pump	7	10-Sep-26	19-Sep-26	07-Sep-26 A	07-Sep-26 A	0.00	0.00	0.00	100%	100%
DAM3-P-ST-M-350	Fire hose cabinet	7	05-Aug-26	12-Aug-26	19-Sep-26 A	20-Sep-26 A	0.00	0.00	0.00	100%	100%
DAM3-P-ST-M-360	Western water closet	7	05-Oct-26	13-Oct-26	19-Sep-26 A	20-Sep-26 A	0.00	0.00	0.00	3.57%	100%
DAM3-P-ST-M-380	Fire pumps	7	16-Sep-26	26-Sep-26	20-Sep-26 A	20-Sep-26 A	0.00	0.00	0.00	100%	100%
SHORT LEAD MATERIALS		258	04-Feb-26	14-Oct-26	14-Jan-26 A	21-Sep-26 A	9,849,294.69	9,845,369.70	9,849,294.69	99.96%	100%
STRUCTURAL		74	04-Feb-26	15-Apr-26	20-Jan-26 A	29-Apr-26 A	3,207,417.90	3,207,417.90	3,207,417.90	100%	100%
PO ISSUE		28	04-Feb-26	15-Feb-26	20-Jan-26 A	25-Mar-26 A	0.00	0.00	0.00	0%	0%
DAM3-P-PO-C-60	Concrete mix	2	07-Feb-26	08-Feb-26	20-Jan-26 A	20-Jan-26 A	0.00	0.00	0.00	100%	100%
DAM3-P-PO-C-90	Rebar	2	14-Feb-26	15-Feb-26	01-Feb-26 A	01-Feb-26 A	0.00	0.00	0.00	100%	100%
DAM3-P-PO-C-70	Polyethylene sheet	2	09-Feb-26	10-Feb-26	01-Mar-26 A	01-Mar-26 A	0.00	0.00	0.00	100%	100%
DAM3-P-PO-C-80	Bitumen paint	2	11-Feb-26	12-Feb-26	09-Mar-26 A	09-Mar-26 A	0.00	0.00	0.00	100%	100%
DAM3-P-PO-C-50	Anti termite	2	04-Feb-26	05-Feb-26	25-Mar-26 A	25-Mar-26 A	0.00	0.00	0.00	100%	100%
MANUFACTURING		38	07-Feb-26	02-Mar-26	21-Jan-26 A	07-Apr-26 A	0.00	0.00	0.00	0%	0%
DAM3-P-MF-C-60	Concrete mix	17	09-Feb-26	02-Mar-26	21-Jan-26 A	01-Feb-26 A	0.00	0.00	0.00	100%	100%
DAM3-P-MF-C-90	Rebar	7	16-Feb-26	25-Feb-26	02-Feb-26 A	15-Feb-26 A	0.00	0.00	0.00	100%	100%
DAM3-P-MF-C-70	Polyethylene sheet	10	09-Feb-26	21-Feb-26	02-Mar-26 A	10-Mar-26 A	0.00	0.00	0.00	100%	100%
DAM3-P-MF-C-80	Bitumen paint	10	14-Feb-26	26-Feb-26	10-Mar-26 A	07-Apr-26 A	0.00	0.00	0.00	100%	100%
DAM3-P-MF-C-50	Anti termite	12	07-Feb-26	21-Feb-26	26-Mar-26 A	07-Apr-26 A	0.00	0.00	0.00	100%	100%
DELIVERY		59	21-Feb-26	15-Apr-26	12-Mar-26 A	29-Apr-26 A	3,207,417.90	3,207,417.90	3,207,417.90	100%	100%
DAM3-P-DL-C-50	Anti termite	2	21-Feb-26	24-Feb-26	12-Mar-26 A	29-Apr-26 A	130,309.59	130,309.59	130,309.59	100%	100%
DAM3-P-DL-C-60	Concrete mix -1	2	03-Mar-26	04-Mar-26	12-Mar-26 A	14-Apr-26 A	196,863.16	196,863.16	196,863.16	100%	100%
DAM3-P-DL-C-70	Polyethylene sheet	2	21-Feb-26	24-Feb-26	12-Mar-26 A	29-Apr-26 A	86,906.55	86,906.55	86,906.55	100%	100%
DAM3-P-DL-C-80	Bitumen paint	2	26-Feb-26	01-Mar-26	31-Mar-26 A	29-Apr-26 A	192,960.68	192,960.68	192,960.68	100%	100%
DAM3-P-DL-C-90	Rebar-1	2	25-Feb-26	28-Feb-26	31-Mar-26 A	29-Apr-26 A	218,896.43	218,896.43	218,896.43	100%	100%
DAM3-P-DL-C-100	Concrete mix -2	2	12-Apr-26	13-Apr-26	16-Apr-26 A	29-Apr-26 A	740,740.74	740,740.74	740,740.74	100%	100%
DAM3-P-DL-C-110	Concrete mix -3	2	14-Apr-26	15-Apr-26	16-Apr-26 A	29-Apr-26 A	740,740.74	740,740.74	740,740.74	100%	100%
DAM3-P-DL-C-120	Rebar-2	2	12-Apr-26	13-Apr-26	16-Apr-26 A	29-Apr-26 A	450,000.00	450,000.00	450,000.00	100%	100%
DAM3-P-DL-C-130	Rebar-3	2	14-Apr-26	15-Apr-26	16-Apr-26 A	29-Apr-26 A	450,000.00	450,000.00	450,000.00	100%	100%
STAGING TIME		16	24-Feb-26	05-Mar-26	12-Mar-26 A	29-Apr-26 A	0.00	0.00	0.00	0%	0%
DAM3-P-ST-C-50	Anti termite	1	24-Feb-26	25-Feb-26	12-Mar-26 A	29-Apr-26 A	0.00	0.00	0.00	100%	100%
DAM3-P-ST-C-60	Concrete mix	1	05-Mar-26	05-Mar-26	12-Mar-26 A	29-Apr-26 A	0.00	0.00	0.00	100%	100%
DAM3-P-ST-C-70	Polyethylene sheet	1	24-Feb-26	25-Feb-26	12-Mar-26 A	29-Apr-26 A	0.00	0.00	0.00	100%	100%
DAM3-P-ST-C-80	Bitumen paint	1	02-Mar-26	02-Mar-26	31-Mar-26 A	29-Apr-26 A	0.00	0.00	0.00	100%	100%
DAM3-P-ST-C-90	Rebar	1	01-Mar-26	01-Mar-26	31-Mar-26 A	29-Apr-26 A	0.00	0.00	0.00	100%	100%
ARCHITECTURAL		107	09-Feb-26	19-Jul-26	14-Jan-26 A	20-Sep-26 A	2,031,043.96	2,031,043.96	2,031,043.96	100%	100%
PO ISSUE		86	09-Feb-26	28-Mar-26	14-Jan-26 A	24-May-26 A	0.00	0.00	0.00	0%	0%
DAM3-P-PO-A-210	Steel ladder	5	15-Feb-26	21-Feb-26	14-Jan-26 A	18-Jan-26 A	0.00	0.00	0.00	100%	100%
DAM3-P-PO-A-220	Steel gratings	5	21-Feb-26	28-Feb-26	02-Apr-26 A	02-Apr-26 A	0.00	0.00	0.00	100%	100%
DAM3-P-PO-A-200	Concrete masonry unit (CMU)	5	09-Feb-26	14-Feb-26	05-Apr-26 A	05-Apr-26 A	0.00	0.00	0.00	100%	100%
DAM3-P-PO-A-320	Interal paint	5	07-Mar-26	12-Mar-26	05-Apr-26 A	05-Apr-26 A	0.00	0.00	0.00	100%	100%
DAM3-P-PO-A-330	Gypsum board	5	12-Mar-26	22-Mar-26	05-Apr-26 A	05-Apr-26 A	0.00	0.00	0.00	100%	100%
DAM3-E-PO-A-1720	Aluminum Composite Panel	5	22-Mar-26	28-Mar-26	05-Apr-26 A	05-Apr-26 A	0.00	0.00	0.00	100%	100%
DAM3-E-PO-A-1750	Steel fence and gates	5	11-Mar-26	16-Mar-26	05-Apr-26 A	05-Apr-26 A	0.00	0.00	0.00	100%	100%
DAM3-E-PO-A-1760	Identification sign; ID01 & ID02	5	21-Mar-26	25-Mar-26	05-Apr-26 A	05-Apr-26 A	0.00	0.00	0.00	100%	100%
DAM3-P-PO-A-280	Ceramic tiles	5	24-Feb-26	02-Mar-26	07-Apr-26 A	07-Apr-26 A	0.00	0.00	0.00	100%	100%
DAM3-P-PO-A-290	Granite strip	5	03-Mar-26	08-Mar-26	12-May-26 A	12-May-26 A	0.00	0.00	0.00	100%	100%
DAM3-P-PO-A-230	Steel rails	5	01-Mar-26	05-Mar-26	24-May-26 A	24-May-26 A	0.00	0.00	0.00	100%	100%

Activity ID	Activity Name	Original Duration	BL Project Start	BL Project Finish	Start	Finish	Budgeted Total Cost	Planned Value Cost	Earned Value Cost	Schedule % Complete	Performance % Complete
DAM3-P-PO-A-310	Epoxy paint	5	01-Mar-26	07-Mar-26	24-May-26 A	24-May-26 A	0.00	0.00	0.00	100%	100%
MANUFACTURING		100	15-Feb-26	02-Jul-26	14-Jan-26 A	19-Sep-26 A	0.00	0.00	0.00	0%	0%
DAM3-P-MF-A-210	Steel ladder	80	21-Feb-26	02-Jun-26	14-Jan-26 A	22-Jul-26 A	0.00	0.00	0.00	100%	100%
DAM3-P-MF-A-200	Concrete masonry unit (CMU)	50	15-Feb-26	19-Apr-26	06-Apr-26 A	08-Jun-26 A	0.00	0.00	0.00	100%	100%
DAM3-P-MF-A-220	Steel gratings	80	01-Mar-26	08-Jun-26	06-Apr-26 A	02-Jul-26 A	0.00	0.00	0.00	100%	100%
DAM3-P-MF-A-230	Steel rails	80	07-Mar-26	14-Jun-26	06-Apr-26 A	02-Jul-26 A	0.00	0.00	0.00	100%	100%
DAM3-P-MF-A-280	Ceramic tiles	80	03-Mar-26	10-Jun-26	06-Apr-26 A	09-Jun-26 A	0.00	0.00	0.00	100%	100%
DAM3-P-MF-A-290	Granite strip	80	09-Mar-26	16-Jun-26	06-Apr-26 A	19-Sep-26 A	0.00	0.00	0.00	100%	100%
DAM3-P-MF-A-310	Epoxy paint	80	07-Mar-26	15-Jun-26	06-Apr-26 A	20-Jul-26 A	0.00	0.00	0.00	100%	100%
DAM3-P-MF-A-320	Interml paint	80	12-Mar-26	21-Jun-26	06-Apr-26 A	19-Sep-26 A	0.00	0.00	0.00	100%	100%
DAM3-P-MF-A-330	Gypsum board	80	22-Mar-26	27-Jun-26	06-Apr-26 A	19-Sep-26 A	0.00	0.00	0.00	100%	100%
DAM3-E-MF-A-1720	Aluminum Composite Panel	80	28-Mar-26	02-Jul-26	06-Apr-26 A	19-Sep-26 A	0.00	0.00	0.00	100%	100%
DAM3-E-MF-A-1750	Steel fence and gates	80	21-Mar-26	24-Jun-26	06-Apr-26 A	19-Sep-26 A	0.00	0.00	0.00	100%	100%
DAM3-E-MF-A-1760	Identification sign; ID01 & ID02	80	26-Mar-26	30-Jun-26	06-Apr-26 A	19-Sep-26 A	0.00	0.00	0.00	100%	100%
DELIVERY		59	20-Apr-26	11-Jul-26	10-Jun-26 A	20-Sep-26 A	2,031,043.96	2,031,043.96	2,031,043.96	100%	100%
DAM3-P-DL-A-200	Concrete masonry unit (CMU)	7	20-Apr-26	27-Apr-26	10-Jun-26 A	14-Jun-26 A	418,802.40	418,802.40	418,802.40	100%	100%
DAM3-P-DL-A-280	Ceramic tiles	7	11-Jun-26	18-Jun-26	11-Jun-26 A	15-Jun-26 A	241,008.42	241,008.42	241,008.42	100%	100%
DAM3-P-DL-A-220	Steel gratings	7	09-Jun-26	16-Jun-26	05-Jul-26 A	05-Jul-26 A	21,196.03	21,196.03	21,196.03	100%	100%
DAM3-P-DL-A-310	Epoxy paint	7	15-Jun-26	23-Jun-26	23-Jul-26 A	25-Jul-26 A	378,990.27	378,990.27	378,990.27	100%	100%
DAM3-P-DL-A-210	Steel ladder	7	03-Jun-26	10-Jun-26	28-Jul-26 A	28-Jul-26 A	32,307.70	32,307.70	32,307.70	100%	100%
DAM3-P-DL-A-230	Steel rails	7	15-Jun-26	22-Jun-26	28-Jul-26 A	28-Jul-26 A	5,036.93	5,036.93	5,036.93	100%	100%
DAM3-P-DL-A-320	Interml paint	7	21-Jun-26	29-Jun-26	02-Sep-26 A	20-Sep-26 A	145,026.96	145,026.96	145,026.96	100%	100%
DAM3-P-DL-A-1720	Aluminum Composite Panel	7	02-Jul-26	11-Jul-26	07-Sep-26 A	20-Sep-26 A	577,545.17	577,545.17	577,545.17	100%	100%
DAM3-P-DL-A-330	Gypsum board	7	27-Jun-26	05-Jul-26	14-Sep-26 A	20-Sep-26 A	153,646.35	153,646.35	153,646.35	100%	100%
DAM3-P-DL-A-290	Granite strip	7	17-Jun-26	24-Jun-26	20-Sep-26 A	20-Sep-26 A	2,203.66	2,203.66	2,203.66	100%	100%
DAM3-P-DL-A-1750	Steel fence and gates	7	25-Jun-26	02-Jul-26	20-Sep-26 A	20-Sep-26 A	23,657.36	23,657.36	23,657.36	100%	100%
DAM3-P-DL-A-1760	Identification sign; ID01 & ID02	7	01-Jul-26	08-Jul-26	20-Sep-26 A	20-Sep-26 A	31,622.71	31,622.71	31,622.71	100%	100%
STAGING TIME		58	28-Apr-26	19-Jul-26	15-Jun-26 A	20-Sep-26 A	0.00	0.00	0.00	0%	0%
DAM3-P-ST-A-200	Concrete masonry unit (CMU)	7	28-Apr-26	05-May-26	15-Jun-26 A	15-Jun-26 A	0.00	0.00	0.00	100%	100%
DAM3-P-ST-A-280	Ceramic tiles	7	20-Jun-26	27-Jun-26	15-Jun-26 A	15-Jun-26 A	0.00	0.00	0.00	100%	100%
DAM3-P-ST-A-220	Steel gratings	7	17-Jun-26	24-Jun-26	05-Jul-26 A	05-Jul-26 A	0.00	0.00	0.00	100%	100%
DAM3-P-ST-A-310	Epoxy paint	7	23-Jun-26	01-Jul-26	23-Jul-26 A	25-Jul-26 A	0.00	0.00	0.00	100%	100%
DAM3-P-ST-A-210	Steel ladder	7	11-Jun-26	18-Jun-26	28-Jul-26 A	28-Jul-26 A	0.00	0.00	0.00	100%	100%
DAM3-P-ST-A-230	Steel rails	7	23-Jun-26	30-Jun-26	28-Jul-26 A	28-Jul-26 A	0.00	0.00	0.00	100%	100%
DAM3-P-ST-A-320	Interml paint	7	29-Jun-26	07-Jul-26	02-Sep-26 A	20-Sep-26 A	0.00	0.00	0.00	100%	100%
DAM3-E-ST-A-1720	Aluminum Composite Panel	7	11-Jul-26	19-Jul-26	07-Sep-26 A	20-Sep-26 A	0.00	0.00	0.00	100%	100%
DAM3-P-ST-A-330	Gypsum board	7	05-Jul-26	13-Jul-26	14-Sep-26 A	20-Sep-26 A	0.00	0.00	0.00	100%	100%
DAM3-P-ST-A-290	Granite strip	7	25-Jun-26	02-Jul-26	20-Sep-26 A	20-Sep-26 A	0.00	0.00	0.00	100%	100%
DAM3-E-ST-A-1750	Steel fence and gates	7	04-Jul-26	11-Jul-26	20-Sep-26 A	20-Sep-26 A	0.00	0.00	0.00	100%	100%
DAM3-E-ST-A-1760	Identification sign; ID01 & ID02	7	09-Jul-26	16-Jul-26	20-Sep-26 A	20-Sep-26 A	0.00	0.00	0.00	100%	100%
MECHANICAL		174	11-Feb-26	14-Oct-26	05-Apr-26 A	20-Sep-26 A	1,190,075.32	1,186,150.33	1,190,075.32	99.67%	100%
PO ISSUE		60	11-Feb-26	12-May-26	05-Apr-26 A	26-Apr-26 A	0.00	0.00	0.00	0%	0%
DAM3-P-PO-M-600	HVAC duct	5	17-Feb-26	24-Feb-26	05-Apr-26 A	05-Apr-26 A	0.00	0.00	0.00	100%	100%
DAM3-P-PO-M-390	Fire fighting valves	5	07-May-26	12-May-26	26-Apr-26 A	26-Apr-26 A	0.00	0.00	0.00	100%	100%
DAM3-P-PO-M-420	Water supply valves	5	18-Apr-26	23-Apr-26	26-Apr-26 A	26-Apr-26 A	0.00	0.00	0.00	100%	100%
DAM3-P-PO-M-430	U/G HDPE pipes	5	09-Mar-26	14-Mar-26	26-Apr-26 A	26-Apr-26 A	0.00	0.00	0.00	100%	100%
DAM3-P-PO-M-440	Automatic air release valve	5	24-Mar-26	29-Mar-26	26-Apr-26 A	26-Apr-26 A	0.00	0.00	0.00	100%	100%
DAM3-P-PO-M-450	OS & Y gate valve	5	30-Mar-26	04-Apr-26	26-Apr-26 A	26-Apr-26 A	0.00	0.00	0.00	100%	100%
DAM3-P-PO-M-460	Fire alarm check valve	5	05-Apr-26	09-Apr-26	26-Apr-26 A	26-Apr-26 A	0.00	0.00	0.00	100%	100%

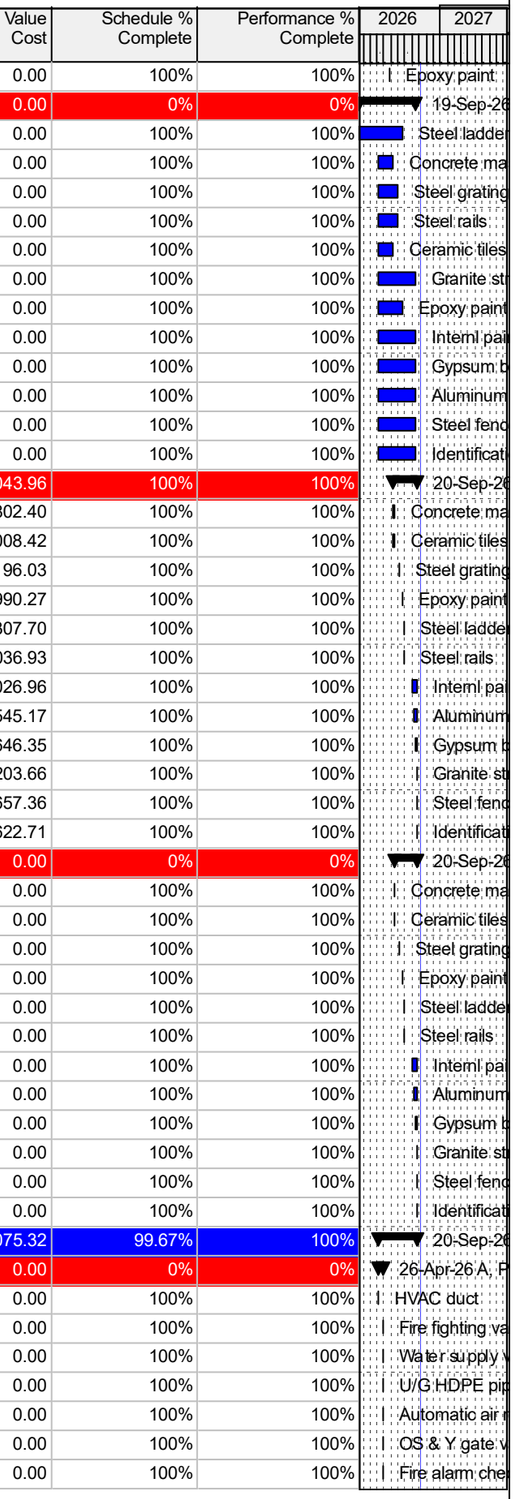

Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary

Date	Revision	Checked	Approved
06-Oct-26	Weekly Report		

Activity ID	Activity Name	Original Duration	BL Project Start	BL Project Finish	Start	Finish	Budgeted Total Cost	Planned Value Cost	Earned Value Cost	Schedule % Complete	Performance % Complete
DAM3-P-PO-M-480	PPR pipes	5	11-Feb-26	16-Feb-26	26-Apr-26 A	26-Apr-26 A	0.00	0.00	0.00	100%	100%
DAM3-P-PO-M-490	Ball valve	5	07-Mar-26	11-Mar-26	26-Apr-26 A	26-Apr-26 A	0.00	0.00	0.00	100%	100%
DAM3-P-PO-M-500	Capped connection	5	12-Mar-26	21-Mar-26	26-Apr-26 A	26-Apr-26 A	0.00	0.00	0.00	100%	100%
DAM3-P-PO-M-510	UPVC pipes	5	22-Mar-26	26-Mar-26	26-Apr-26 A	26-Apr-26 A	0.00	0.00	0.00	100%	100%
DAM3-P-PO-M-520	Roof vent caps	5	28-Mar-26	01-Apr-26	26-Apr-26 A	26-Apr-26 A	0.00	0.00	0.00	100%	100%
DAM3-P-PO-M-530	Floor drain	5	02-Apr-26	07-Apr-26	26-Apr-26 A	26-Apr-26 A	0.00	0.00	0.00	100%	100%
DAM3-P-PO-M-540	Gully trap	5	08-Apr-26	13-Apr-26	26-Apr-26 A	26-Apr-26 A	0.00	0.00	0.00	100%	100%
DAM3-P-PO-M-550	Electric water heater	5	14-Apr-26	19-Apr-26	26-Apr-26 A	26-Apr-26 A	0.00	0.00	0.00	100%	100%
DAM3-P-PO-M-560	Bib tap	5	20-Apr-26	25-Apr-26	26-Apr-26 A	26-Apr-26 A	0.00	0.00	0.00	100%	100%
DAM3-P-PO-M-580	Lavatory / wash basin	5	26-Apr-26	30-Apr-26	26-Apr-26 A	26-Apr-26 A	0.00	0.00	0.00	100%	100%
DAM3-P-PO-M-590	Inline exhaust fans	5	02-May-26	06-May-26	26-Apr-26 A	26-Apr-26 A	0.00	0.00	0.00	100%	100%
DAM3-P-PO-M-610	Flexible duct	5	24-Feb-26	02-Mar-26	26-Apr-26 A	26-Apr-26 A	0.00	0.00	0.00	100%	100%
DAM3-P-PO-M-620	Exhaust diffuser	5	03-Mar-26	08-Mar-26	26-Apr-26 A	26-Apr-26 A	0.00	0.00	0.00	100%	100%
DAM3-P-PO-M-660	Warning tapes	5	15-Mar-26	23-Mar-26	26-Apr-26 A	26-Apr-26 A	0.00	0.00	0.00	100%	100%
DAM3-E-PO-M-3410	Water tap	5	21-Apr-26	26-Apr-26	26-Apr-26 A	26-Apr-26 A	0.00	0.00	0.00	100%	100%
DAM3-P-PO-M-570	Toilet Fittings	5	30-Mar-26	05-Apr-26	26-Apr-26 A	26-Apr-26 A	0.00	0.00	0.00	100%	100%
MANUFACTURING		169	17-Feb-26	28-Sep-26	06-Apr-26 A	19-Sep-26 A	0.00	0.00	0.00	0%	0%
DAM3-P-MF-M-600	HVAC duct	80	24-Feb-26	04-Jun-26	06-Apr-26 A	01-Jun-26 A	0.00	0.00	0.00	100%	100%
DAM3-P-MF-M-390	Fire fighting valves	80	13-May-26	17-Aug-26	27-Apr-26 A	09-Aug-26 A	0.00	0.00	0.00	100%	100%
DAM3-P-MF-M-420	Water supply valves	80	23-Apr-26	29-Jul-26	27-Apr-26 A	02-Aug-26 A	0.00	0.00	0.00	100%	100%
DAM3-P-MF-M-430	U/G HDPE pipes	80	15-Mar-26	22-Jun-26	27-Apr-26 A	02-Aug-26 A	0.00	0.00	0.00	100%	100%
DAM3-P-MF-M-440	Automatic air release valve	80	30-Mar-26	04-Jul-26	27-Apr-26 A	19-Sep-26 A	0.00	0.00	0.00	100%	100%
DAM3-P-MF-M-450	OS & Y gate valve	80	05-Apr-26	09-Jul-26	27-Apr-26 A	19-Sep-26 A	0.00	0.00	0.00	100%	100%
DAM3-P-MF-M-460	Fire alarm check valve	80	11-Apr-26	15-Jul-26	27-Apr-26 A	19-Sep-26 A	0.00	0.00	0.00	100%	100%
DAM3-P-MF-M-480	PPR pipes	80	17-Feb-26	30-May-26	27-Apr-26 A	03-Aug-26 A	0.00	0.00	0.00	100%	100%
DAM3-P-MF-M-490	Ball valve	80	12-Mar-26	20-Jun-26	27-Apr-26 A	19-Sep-26 A	0.00	0.00	0.00	100%	100%
DAM3-P-MF-M-500	Capped connection	80	22-Mar-26	25-Jun-26	27-Apr-26 A	19-Sep-26 A	0.00	0.00	0.00	100%	100%
DAM3-P-MF-M-510	UPVC pipes	80	28-Mar-26	01-Jul-26	27-Apr-26 A	19-Sep-26 A	0.00	0.00	0.00	100%	100%
DAM3-P-MF-M-520	Roof vent caps	80	02-Apr-26	07-Jul-26	27-Apr-26 A	19-Sep-26 A	0.00	0.00	0.00	100%	100%
DAM3-P-MF-M-530	Floor drain	80	08-Apr-26	13-Jul-26	27-Apr-26 A	19-Sep-26 A	0.00	0.00	0.00	100%	100%
DAM3-P-MF-M-540	Gully trap	80	14-Apr-26	19-Jul-26	27-Apr-26 A	19-Sep-26 A	0.00	0.00	0.00	100%	100%
DAM3-P-MF-M-550	Electric water heater	120	20-Apr-26	09-Sep-26	27-Apr-26 A	13-Sep-26 A	0.00	0.00	0.00	100%	100%
DAM3-P-MF-M-560	Bib tap	80	26-Apr-26	30-Jul-26	27-Apr-26 A	19-Sep-26 A	0.00	0.00	0.00	100%	100%
DAM3-P-MF-M-580	Lavatory / wash basin	80	02-May-26	05-Aug-26	27-Apr-26 A	19-Sep-26 A	0.00	0.00	0.00	100%	100%
DAM3-P-MF-M-590	Inline exhaust fans	120	07-May-26	28-Sep-26	27-Apr-26 A	19-Sep-26 A	0.00	0.00	0.00	100%	100%
DAM3-P-MF-M-610	Flexible duct	80	03-Mar-26	10-Jun-26	27-Apr-26 A	19-Sep-26 A	0.00	0.00	0.00	100%	100%
DAM3-P-MF-M-620	Exhaust diffuser	80	09-Mar-26	16-Jun-26	27-Apr-26 A	19-Sep-26 A	0.00	0.00	0.00	100%	100%
DAM3-P-MF-M-660	Warning tapes	80	24-Mar-26	28-Jun-26	27-Apr-26 A	19-Sep-26 A	0.00	0.00	0.00	100%	100%
DAM3-E-MF-M-3410	Water tap	80	27-Apr-26	01-Aug-26	27-Apr-26 A	19-Sep-26 A	0.00	0.00	0.00	100%	100%
DAM3-P-MF-M-570	Toilet Fittings	5	05-Apr-26	11-Apr-26	27-Apr-26 A	19-Sep-26 A	0.00	0.00	0.00	100%	100%
DELIVERY		60	11-Apr-26	06-Oct-26	10-May-26 A	20-Sep-26 A	1,190,075.32	1,186,150.33	1,190,075.32	99.67%	100%
DAM3-P-DL-M-510	UPVC pipes	7	02-Jul-26	09-Jul-26	10-May-26 A	19-May-26 A	126,693.12	126,693.12	126,693.12	100%	100%
DAM3-P-DL-M-600	HVAC duct	7	06-Jun-26	13-Jun-26	04-Jun-26 A	14-Jun-26 A	490,860.48	490,860.48	490,860.48	100%	100%
DAM3-P-DL-M-420	Water supply valves	7	29-Jul-26	06-Aug-26	05-Jul-26 A	15-Sep-26 A	3,114.56	3,114.56	3,114.56	100%	100%
DAM3-P-DL-M-480	PPR pipes	7	31-May-26	07-Jun-26	05-Jul-26 A	15-Sep-26 A	76,567.93	76,567.93	76,567.93	100%	100%
DAM3-P-DL-M-500	Capped connection	7	27-Jun-26	04-Jul-26	05-Jul-26 A	14-Sep-26 A	913.27	913.27	913.27	100%	100%
DAM3-P-DL-M-660	Warning tapes	7	29-Jun-26	06-Jul-26	05-Jul-26 A	05-Jul-26 A	14,077.01	14,077.01	14,077.01	100%	100%
DAM3-P-DL-M-450	OS & Y gate valve	7	11-Jul-26	18-Jul-26	15-Jul-26 A	20-Sep-26 A	11,631.51	11,631.51	11,631.51	100%	100%
DAM3-P-DL-M-490	Ball valve	7	21-Jun-26	28-Jun-26	18-Jul-26 A	18-Jul-26 A	14,232.16	14,232.16	14,232.16	100%	100%

2026 2027

PPR pipes
Ball valve
Capped conne
UPVC pipes
Roof vent cap
Floor drain
Gully trap
Electric water h
Bib tap
Lavatory / was
Inline exhaust
Flexible duct
Exhaust diffus
Warning tapes
Water tap
Toilet Fittings
19-Sep-26
HVAC duct
Fire fighting
Water supp
U/G HDPE
Automatic
OS & Y ga
Fire alarm
PPR pipes
Ball valve
Capped c
UPVC pip
Roof vent
Floor drain
Gully trap
Electric wa
Bib tap
Lavatory /
Inline exha
Flexible du
Exhaust d
Warning ta
Water tap
Toilet Fittin
20-Sep-26
UPVC pipes
HVAC duct
Water sup
PPR pipes
Capped c
Warning tap
OS & Y ga
Ball valve

Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary

Date	Revision	Checked	Approved
06-Oct-26	Weekly Report		

Activity ID	Activity Name	Original Duration	BL Project Start	BL Project Finish	Start	Finish	Budgeted Total Cost	Planned Value Cost	Earned Value Cost	Schedule % Complete	Performance % Complete
DAM3-P-DL-M-430	U/G HDPE pipes	7	23-Jun-26	30-Jun-26	01-Aug-26 A	20-Sep-26 A	49,971.54	49,971.54	49,971.54	100%	100%
DAM3-P-DL-M-390	Fire fighting valves	7	18-Aug-26	25-Aug-26	10-Aug-26 A	10-Aug-26 A	8,885.58	8,885.58	8,885.58	100%	100%
DAM3-P-DL-M-590	Inline exhaust fans	7	29-Sep-26	06-Oct-26	05-Sep-26 A	20-Sep-26 A	27,474.92	23,549.93	27,474.92	85.71%	100%
DAM3-P-DL-M-540	Gully trap	7	20-Jul-26	27-Jul-26	06-Sep-26 A	20-Sep-26 A	15,982.56	15,982.56	15,982.56	100%	100%
DAM3-P-DL-M-570	Toilet Fittings	5	11-Apr-26	16-Apr-26	15-Sep-26 A	20-Sep-26 A	75,460.88	75,460.88	75,460.88	100%	100%
DAM3-P-DL-M-530	Floor drain	7	14-Jul-26	21-Jul-26	16-Sep-26 A	20-Sep-26 A	74,093.27	74,093.27	74,093.27	100%	100%
DAM3-P-DL-M-550	Electric water heater	7	10-Sep-26	17-Sep-26	16-Sep-26 A	16-Sep-26 A	5,974.50	5,974.50	5,974.50	100%	100%
DAM3-P-DL-M-580	Lavatory / wash basin	7	06-Aug-26	13-Aug-26	16-Sep-26 A	20-Sep-26 A	70,323.44	70,323.44	70,323.44	100%	100%
DAM3-P-DL-M-610	Flexible duct	7	11-Jun-26	18-Jun-26	16-Sep-26 A	20-Sep-26 A	69,629.67	69,629.67	69,629.67	100%	100%
DAM3-P-DL-M-440	Automatic air release valve	7	05-Jul-26	12-Jul-26	20-Sep-26 A	20-Sep-26 A	1,769.50	1,769.50	1,769.50	100%	100%
DAM3-P-DL-M-460	Fire alarm check valve	7	16-Jul-26	23-Jul-26	20-Sep-26 A	20-Sep-26 A	26,656.72	26,656.72	26,656.72	100%	100%
DAM3-P-DL-M-520	Roof vent caps	7	08-Jul-26	15-Jul-26	20-Sep-26 A	20-Sep-26 A	3,044.27	3,044.27	3,044.27	100%	100%
DAM3-P-DL-M-560	Bib tap	7	01-Aug-26	08-Aug-26	20-Sep-26 A	20-Sep-26 A	6,240.96	6,240.96	6,240.96	100%	100%
DAM3-P-DL-M-620	Exhaust diffuser	7	17-Jun-26	24-Jun-26	20-Sep-26 A	20-Sep-26 A	7,040.00	7,040.00	7,040.00	100%	100%
DAM3-P-DL-M-3410	Water tap	7	02-Aug-26	09-Aug-26	20-Sep-26 A	20-Sep-26 A	9,437.47	9,437.47	9,437.47	100%	100%
STAGING TIME		67	16-Apr-26	14-Oct-26	10-May-26 A	20-Sep-26 A	0.00	0.00	0.00	0%	0%
DAM3-P-ST-M-510	UPVC pipes	7	11-Jul-26	18-Jul-26	10-May-26 A	19-May-26 A	0.00	0.00	0.00	100%	100%
DAM3-P-ST-M-600	HVAC duct	7	14-Jun-26	21-Jun-26	04-Jun-26 A	14-Jun-26 A	0.00	0.00	0.00	100%	100%
DAM3-P-ST-M-420	Water supply valves	7	06-Aug-26	15-Aug-26	05-Jul-26 A	15-Sep-26 A	0.00	0.00	0.00	100%	100%
DAM3-P-ST-M-480	PPR pipes	7	08-Jun-26	15-Jun-26	05-Jul-26 A	15-Sep-26 A	0.00	0.00	0.00	100%	100%
DAM3-P-ST-M-500	Capped connection	7	05-Jul-26	12-Jul-26	05-Jul-26 A	14-Sep-26 A	0.00	0.00	0.00	100%	100%
DAM3-P-ST-M-660	Warning tapes	7	07-Jul-26	14-Jul-26	05-Jul-26 A	05-Jul-26 A	0.00	0.00	0.00	100%	100%
DAM3-P-ST-M-450	OS & Y gate valve	7	19-Jul-26	26-Jul-26	15-Jul-26 A	20-Sep-26 A	0.00	0.00	0.00	100%	100%
DAM3-P-ST-M-490	Ball valve	7	29-Jun-26	06-Jul-26	18-Jul-26 A	18-Jul-26 A	0.00	0.00	0.00	100%	100%
DAM3-P-ST-M-430	U/G HDPE pipes	7	01-Jul-26	08-Jul-26	01-Aug-26 A	20-Sep-26 A	0.00	0.00	0.00	100%	100%
DAM3-P-ST-M-390	Fire fighting valves	7	26-Aug-26	02-Sep-26	10-Aug-26 A	10-Aug-26 A	0.00	0.00	0.00	100%	100%
DAM3-P-ST-M-590	Inline exhaust fans	7	07-Oct-26	14-Oct-26	05-Sep-26 A	20-Sep-26 A	0.00	0.00	0.00	0%	100%
DAM3-P-ST-M-540	Gully trap	7	28-Jul-26	04-Aug-26	06-Sep-26 A	20-Sep-26 A	0.00	0.00	0.00	100%	100%
DAM3-P-ST-M-570	Toilet Fittings	5	16-Apr-26	22-Apr-26	15-Sep-26 A	20-Sep-26 A	0.00	0.00	0.00	100%	100%
DAM3-P-ST-M-530	Floor drain	7	22-Jul-26	29-Jul-26	16-Sep-26 A	20-Sep-26 A	0.00	0.00	0.00	100%	100%
DAM3-P-ST-M-550	Electric water heater	7	19-Sep-26	27-Sep-26	16-Sep-26 A	16-Sep-26 A	0.00	0.00	0.00	100%	100%
DAM3-P-ST-M-580	Lavatory / wash basin	7	15-Aug-26	22-Aug-26	16-Sep-26 A	20-Sep-26 A	0.00	0.00	0.00	100%	100%
DAM3-P-ST-M-610	Flexible duct	7	20-Jun-26	27-Jun-26	16-Sep-26 A	20-Sep-26 A	0.00	0.00	0.00	100%	100%
DAM3-P-ST-M-440	Automatic air release valve	7	13-Jul-26	20-Jul-26	20-Sep-26 A	20-Sep-26 A	0.00	0.00	0.00	100%	100%
DAM3-P-ST-M-460	Fire alarm check valve	7	25-Jul-26	01-Aug-26	20-Sep-26 A	20-Sep-26 A	0.00	0.00	0.00	100%	100%
DAM3-P-ST-M-520	Roof vent caps	7	16-Jul-26	23-Jul-26	20-Sep-26 A	20-Sep-26 A	0.00	0.00	0.00	100%	100%
DAM3-P-ST-M-560	Bib tap	7	09-Aug-26	16-Aug-26	20-Sep-26 A	20-Sep-26 A	0.00	0.00	0.00	100%	100%
DAM3-P-ST-M-620	Exhaust diffuser	7	25-Jun-26	02-Jul-26	20-Sep-26 A	20-Sep-26 A	0.00	0.00	0.00	100%	100%
DAM3-E-ST-M-3410	Water tap	7	10-Aug-26	17-Aug-26	20-Sep-26 A	20-Sep-26 A	0.00	0.00	0.00	100%	100%
ELECTRICAL		147	11-Feb-26	01-Aug-26	10-Mar-26 A	20-Sep-26 A	819,995.13	819,995.13	819,995.13	100%	100%
PO ISSUE		68	11-Feb-26	09-Apr-26	10-Mar-26 A	21-Jun-26 A	0.00	0.00	0.00	0%	0%
DAM3-P-PO-E-310	PVC conduits	5	11-Feb-26	16-Feb-26	10-Mar-26 A	10-Mar-26 A	0.00	0.00	0.00	100%	100%
DAM3-P-PO-E-340	Grounding system	5	03-Mar-26	08-Mar-26	26-Apr-26 A	26-Apr-26 A	0.00	0.00	0.00	100%	100%
DAM3-P-PO-E-370	HDPE ducts	5	15-Mar-26	23-Mar-26	26-Apr-26 A	26-Apr-26 A	0.00	0.00	0.00	100%	100%
DAM3-P-PO-E-290	Low Voltage cables	5	24-Mar-26	29-Mar-26	21-Jun-26 A	21-Jun-26 A	0.00	0.00	0.00	100%	100%
DAM3-P-PO-E-300	Disconnect switches	5	30-Mar-26	04-Apr-26	21-Jun-26 A	21-Jun-26 A	0.00	0.00	0.00	100%	100%
DAM3-P-PO-E-320	Wires	5	17-Feb-26	24-Feb-26	21-Jun-26 A	21-Jun-26 A	0.00	0.00	0.00	100%	100%
DAM3-P-PO-E-330	Wall mounted, duplex, telephone and data outlet	5	05-Apr-26	09-Apr-26	21-Jun-26 A	21-Jun-26 A	0.00	0.00	0.00	100%	100%
DAM3-P-PO-E-350	Wiring devices	5	09-Mar-26	14-Mar-26	21-Jun-26 A	21-Jun-26 A	0.00	0.00	0.00	100%	100%

2026 2027

Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary

Date	Revision	Checked	Approved
06-Oct-26	Weekly Report		

Activity ID	Activity Name	Original Duration	BL Project Start	BL Project Finish	Start	Finish	Budgeted Total Cost	Planned Value Cost	Earned Value Cost	Schedule % Complete	Performance % Complete
DAM3-E-PO-E-210	Cable Tray	5	24-Feb-26	02-Mar-26	21-Jun-26 A	21-Jun-26 A	0.00	0.00	0.00	100%	100%
MANUFACTURING		142	17-Feb-26	15-Jul-26	11-Mar-26 A	16-Sep-26 A	0.00	0.00	0.00	0%	0%
DAM3-P-MF-E-310	PVC conduits	60	17-Feb-26	03-May-26	11-Mar-26 A	02-May-26 A	0.00	0.00	0.00	100%	100%
DAM3-P-MF-E-340	Grounding system	80	09-Mar-26	16-Jun-26	27-Apr-26 A	03-May-26 A	0.00	0.00	0.00	100%	100%
DAM3-P-MF-E-370	HDPE ducts	80	24-Mar-26	28-Jun-26	27-Apr-26 A	03-May-26 A	0.00	0.00	0.00	100%	100%
DAM3-P-MF-E-320	Wires	80	24-Feb-26	04-Jun-26	28-Jun-26 A	16-Sep-26 A	0.00	0.00	0.00	100%	100%
DAM3-E-MF-E-210	Cable Tray	80	03-Mar-26	10-Jun-26	04-Jul-26 A	16-Sep-26 A	0.00	0.00	0.00	100%	100%
DAM3-P-MF-E-350	Wiring devices	80	15-Mar-26	22-Jun-26	09-Jul-26 A	16-Sep-26 A	0.00	0.00	0.00	100%	100%
DAM3-P-MF-E-290	Low Voltage cables	80	30-Mar-26	04-Jul-26	15-Jul-26 A	22-Jul-26 A	0.00	0.00	0.00	100%	100%
DAM3-P-MF-E-300	Disconnect switches	80	05-Apr-26	09-Jul-26	21-Jul-26 A	22-Jul-26 A	0.00	0.00	0.00	100%	100%
DAM3-P-MF-E-330	Wall mounted, duplex, telephone and data outlet	80	11-Apr-26	15-Jul-26	27-Jul-26 A	16-Sep-26 A	0.00	0.00	0.00	100%	100%
DELIVERY		65	04-May-26	23-Jul-26	03-May-26 A	20-Sep-26 A	819,995.13	819,995.13	819,995.13	100%	100%
DAM3-P-DL-E-310	PVC conduits	7	04-May-26	11-May-26	03-May-26 A	20-May-26 A	15,738.66	15,738.66	15,738.66	100%	100%
DAM3-P-DL-E-340	Grounding system	7	17-Jun-26	24-Jun-26	10-May-26 A	19-May-26 A	65,141.26	65,141.26	65,141.26	100%	100%
DAM3-P-DL-E-370	HDPE ducts	7	29-Jun-26	06-Jul-26	10-May-26 A	19-May-26 A	176,019.75	176,019.75	176,019.75	100%	100%
DAM3-P-DL-E-290	Low Voltage cables	7	05-Jul-26	12-Jul-26	23-Jul-26 A	25-Jul-26 A	299,034.47	299,034.47	299,034.47	100%	100%
DAM3-P-DL-E-300	Disconnect switches	7	11-Jul-26	18-Jul-26	23-Jul-26 A	25-Jul-26 A	100,576.04	100,576.04	100,576.04	100%	100%
DAM3-P-DL-E-330	Wall mounted, duplex, telephone and data outlet	7	16-Jul-26	23-Jul-26	17-Sep-26 A	20-Sep-26 A	88,627.44	88,627.44	88,627.44	100%	100%
DAM3-P-DL-E-350	Wiring devices	7	23-Jun-26	30-Jun-26	17-Sep-26 A	20-Sep-26 A	66,414.34	66,414.34	66,414.34	100%	100%
DAM3-P-DL-E-320	Wires	7	06-Jun-26	13-Jun-26	20-Sep-26 A	20-Sep-26 A	7,379.37	7,379.37	7,379.37	100%	100%
DAM3-P-DL-E-2100	Cable Tray	7	11-Jun-26	18-Jun-26	20-Sep-26 A	20-Sep-26 A	1,063.80	1,063.80	1,063.80	100%	100%
STAGING TIME		75	12-May-26	01-Aug-26	03-May-26 A	20-Sep-26 A	0.00	0.00	0.00	0%	0%
DAM3-P-ST-E-310	PVC conduits	7	12-May-26	19-May-26	03-May-26 A	20-May-26 A	0.00	0.00	0.00	100%	100%
DAM3-P-ST-E-340	Grounding system	7	25-Jun-26	02-Jul-26	10-May-26 A	19-May-26 A	0.00	0.00	0.00	100%	100%
DAM3-P-ST-E-370	HDPE ducts	7	07-Jul-26	14-Jul-26	10-May-26 A	19-May-26 A	0.00	0.00	0.00	100%	100%
DAM3-P-ST-E-290	Low Voltage cables	7	13-Jul-26	20-Jul-26	25-Jul-26 A	25-Jul-26 A	0.00	0.00	0.00	100%	100%
DAM3-P-ST-E-300	Disconnect switches	7	19-Jul-26	26-Jul-26	25-Jul-26 A	25-Jul-26 A	0.00	0.00	0.00	100%	100%
DAM3-P-ST-E-330	Wall mounted, duplex, telephone and data outlet	7	25-Jul-26	01-Aug-26	17-Sep-26 A	20-Sep-26 A	0.00	0.00	0.00	100%	100%
DAM3-P-ST-E-350	Wiring devices	7	01-Jul-26	08-Jul-26	17-Sep-26 A	20-Sep-26 A	0.00	0.00	0.00	100%	100%
DAM3-P-ST-E-320	Wires	7	14-Jun-26	21-Jun-26	20-Sep-26 A	20-Sep-26 A	0.00	0.00	0.00	100%	100%
DAM3-E-ST-E-210	Cable Tray	7	20-Jun-26	27-Jun-26	20-Sep-26 A	20-Sep-26 A	0.00	0.00	0.00	100%	100%
EXTERNAL		119	07-Apr-26	03-Sep-26	02-Mar-26 A	21-Sep-26 A	2,215,885.18	2,215,885.18	2,215,885.18	100%	100%
PO ISSUE		23	07-Apr-26	28-Apr-26	02-Mar-26 A	21-Jun-26 A	0.00	0.00	0.00	0%	0%
DAM3-P-PO-EX-80	Asphalt works	5	07-Apr-26	12-Apr-26	02-Mar-26 A	02-Mar-26 A	0.00	0.00	0.00	100%	100%
DAM3-P-PO-EX-90	Concrete parking bumper	5	08-Apr-26	14-Apr-26	21-Jun-26 A	21-Jun-26 A	0.00	0.00	0.00	100%	100%
DAM3-P-PO-EX-100	Road markings	5	11-Apr-26	16-Apr-26	21-Jun-26 A	21-Jun-26 A	0.00	0.00	0.00	100%	100%
DAM3-P-PO-EX-110	Road signs	5	13-Apr-26	19-Apr-26	21-Jun-26 A	21-Jun-26 A	0.00	0.00	0.00	100%	100%
DAM3-P-PO-EX-130	Interlock tiles	5	22-Apr-26	28-Apr-26	21-Jun-26 A	21-Jun-26 A	0.00	0.00	0.00	100%	100%
DAM3-P-PO-EX-140	Curbstones	5	18-Apr-26	23-Apr-26	21-Jun-26 A	21-Jun-26 A	0.00	0.00	0.00	100%	100%
DAM3-P-PO-EX-150	Gravel bedding	5	21-Apr-26	26-Apr-26	21-Jun-26 A	21-Jun-26 A	0.00	0.00	0.00	100%	100%
MANUFACTURING		111	13-Apr-26	15-Aug-26	03-Mar-26 A	20-Sep-26 A	0.00	0.00	0.00	0%	0%
DAM3-P-MF-EX-80	Asphalt works	100	13-Apr-26	10-Aug-26	03-Mar-26 A	07-Jun-26 A	0.00	0.00	0.00	100%	100%
DAM3-P-MF-EX-90	Concrete parking bumper	90	14-Apr-26	01-Aug-26	28-Jun-26 A	19-Sep-26 A	0.00	0.00	0.00	100%	100%
DAM3-P-MF-EX-100	Road markings	90	16-Apr-26	03-Aug-26	28-Jun-26 A	19-Sep-26 A	0.00	0.00	0.00	100%	100%
DAM3-P-MF-EX-110	Road signs	90	19-Apr-26	05-Aug-26	28-Jun-26 A	17-Sep-26 A	0.00	0.00	0.00	100%	100%
DAM3-P-MF-EX-140	Curbstones	90	23-Apr-26	10-Aug-26	28-Jun-26 A	20-Sep-26 A	0.00	0.00	0.00	100%	100%
DAM3-P-MF-EX-150	Gravel bedding	90	27-Apr-26	12-Aug-26	28-Jun-26 A	20-Sep-26 A	0.00	0.00	0.00	100%	100%
DAM3-P-MF-EX-130	Interlock tiles	90	28-Apr-26	15-Aug-26	21-Jul-26 A	20-Sep-26 A	0.00	0.00	0.00	100%	100%
DELIVERY		27	01-Aug-26	23-Aug-26	08-Jun-26 A	21-Sep-26 A	2,215,885.18	2,215,885.18	2,215,885.18	100%	100%

2026 2027

Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary

Date	Revision	Checked	Approved
06-Oct-26	Weekly Report		

Activity ID	Activity Name	Original Duration	BL Project Start	BL Project Finish	Start	Finish	Budgeted Total Cost	Planned Value Cost	Earned Value Cost	Schedule % Complete	Performance % Complete
DAM3-P-DL-EX-80	Asphalt works	7	11-Aug-26	18-Aug-26	08-Jun-26 A	17-Jun-26 A	1,868,985.04	1,868,985.04	1,868,985.04	100%	100%
DAM3-P-DL-EX-130	Interlock tiles	7	15-Aug-26	23-Aug-26	17-Sep-26 A	20-Sep-26 A	141,980.16	141,980.16	141,980.16	100%	100%
DAM3-P-DL-EX-140	Curbstones	7	10-Aug-26	18-Aug-26	17-Sep-26 A	20-Sep-26 A	86,912.40	86,912.40	86,912.40	100%	100%
DAM3-P-DL-EX-150	Gravel bedding	7	13-Aug-26	20-Aug-26	17-Sep-26 A	21-Sep-26 A	66,111.93	66,111.93	66,111.93	100%	100%
DAM3-P-DL-EX-110	Road signs	7	05-Aug-26	13-Aug-26	20-Sep-26 A	20-Sep-26 A	31,028.59	31,028.59	31,028.59	100%	100%
DAM3-P-DL-EX-90	Concrete parking bumper	7	01-Aug-26	09-Aug-26	21-Sep-26 A	21-Sep-26 A	9,558.14	9,558.14	9,558.14	100%	100%
DAM3-P-DL-EX-100	Road markings	7	03-Aug-26	11-Aug-26	21-Sep-26 A	21-Sep-26 A	11,308.91	11,308.91	11,308.91	100%	100%
STAGING TIME		41	09-Aug-26	03-Sep-26	08-Jun-26 A	21-Sep-26 A	0.00	0.00	0.00	0%	0%
DAM3-P-ST-EX-80	Asphalt works	7	19-Aug-26	26-Aug-26	08-Jun-26 A	08-Jun-26 A	0.00	0.00	0.00	100%	100%
DAM3-P-ST-EX-130	Interlock tiles	7	23-Aug-26	31-Aug-26	17-Sep-26 A	20-Sep-26 A	0.00	0.00	0.00	100%	100%
DAM3-P-ST-EX-140	Curbstones	7	27-Aug-26	03-Sep-26	17-Sep-26 A	20-Sep-26 A	0.00	0.00	0.00	100%	100%
DAM3-P-ST-EX-150	Gravel bedding	7	22-Aug-26	29-Aug-26	17-Sep-26 A	21-Sep-26 A	0.00	0.00	0.00	100%	100%
DAM3-P-ST-EX-110	Road signs	7	13-Aug-26	22-Aug-26	20-Sep-26 A	20-Sep-26 A	0.00	0.00	0.00	100%	100%
DAM3-P-ST-EX-90	Concrete parking bumper	7	09-Aug-26	17-Aug-26	21-Sep-26 A	21-Sep-26 A	0.00	0.00	0.00	100%	100%
DAM3-P-ST-EX-100	Road markings	7	11-Aug-26	19-Aug-26	21-Sep-26 A	21-Sep-26 A	0.00	0.00	0.00	100%	100%
ENVIRONMENTAL		151	11-Feb-26	06-Aug-26	21-Jun-26 A	20-Sep-26 A	384,877.22	384,877.22	384,877.22	100%	100%
PO ISSUE		40	11-Feb-26	04-Apr-26	21-Jun-26 A	21-Jun-26 A	0.00	0.00	0.00	0%	0%
DAM3-P-PO-EN-100	HDPE pipes for fire system	5	11-Feb-26	16-Feb-26	21-Jun-26 A	21-Jun-26 A	0.00	0.00	0.00	100%	100%
DAM3-P-PO-EN-110	Directly buried gate valve for fire system	5	17-Feb-26	24-Feb-26	21-Jun-26 A	21-Jun-26 A	0.00	0.00	0.00	100%	100%
DAM3-P-PO-EN-120	HDPE pipes for water supply system	5	24-Feb-26	02-Mar-26	21-Jun-26 A	21-Jun-26 A	0.00	0.00	0.00	100%	100%
DAM3-P-PO-EN-130	Directly buried gate valve for water system	5	03-Mar-26	08-Mar-26	21-Jun-26 A	21-Jun-26 A	0.00	0.00	0.00	100%	100%
DAM3-P-PO-EN-140	Air valve	5	09-Mar-26	14-Mar-26	21-Jun-26 A	21-Jun-26 A	0.00	0.00	0.00	100%	100%
DAM3-P-PO-EN-150	Washout valve	5	15-Mar-26	23-Mar-26	21-Jun-26 A	21-Jun-26 A	0.00	0.00	0.00	100%	100%
DAM3-P-PO-EN-160	Gate valve	5	24-Mar-26	29-Mar-26	21-Jun-26 A	21-Jun-26 A	0.00	0.00	0.00	100%	100%
DAM3-P-PO-EN-170	UPVC pipes	5	30-Mar-26	04-Apr-26	21-Jun-26 A	21-Jun-26 A	0.00	0.00	0.00	100%	100%
MANUFACTURING		133	17-Feb-26	21-Jul-26	22-Jun-26 A	19-Sep-26 A	0.00	0.00	0.00	0%	0%
DAM3-P-MF-EN-120	HDPE pipes for water supply system	90	03-Mar-26	22-Jun-26	22-Jun-26 A	15-Aug-26 A	0.00	0.00	0.00	100%	100%
DAM3-P-MF-EN-130	Directly buried gate valve for water system	90	09-Mar-26	28-Jun-26	22-Jun-26 A	19-Sep-26 A	0.00	0.00	0.00	100%	100%
DAM3-P-MF-EN-140	Air valve	90	15-Mar-26	04-Jul-26	22-Jun-26 A	19-Sep-26 A	0.00	0.00	0.00	100%	100%
DAM3-P-MF-EN-150	Washout valve	90	24-Mar-26	09-Jul-26	22-Jun-26 A	19-Sep-26 A	0.00	0.00	0.00	100%	100%
DAM3-P-MF-EN-160	Gate valve	90	30-Mar-26	15-Jul-26	22-Jun-26 A	19-Sep-26 A	0.00	0.00	0.00	100%	100%
DAM3-P-MF-EN-170	UPVC pipes	90	05-Apr-26	21-Jul-26	22-Jun-26 A	25-Jul-26 A	0.00	0.00	0.00	100%	100%
DAM3-P-MF-EN-100	HDPE pipes for fire system	90	17-Feb-26	10-Jun-26	28-Jun-26 A	23-Jul-26 A	0.00	0.00	0.00	100%	100%
DAM3-P-MF-EN-110	Directly buried gate valve for fire system	90	24-Feb-26	16-Jun-26	04-Jul-26 A	19-Sep-26 A	0.00	0.00	0.00	100%	100%
DELIVERY		107	11-Jun-26	29-Jul-26	25-Jul-26 A	20-Sep-26 A	384,877.22	384,877.22	384,877.22	100%	100%
DAM3-P-DL-EN-100	HDPE pipes for fire system	7	11-Jun-26	18-Jun-26	25-Jul-26 A	26-Jul-26 A	144,972.85	144,972.85	144,972.85	100%	100%
DAM3-P-DL-EN-170	UPVC pipes	7	22-Jul-26	29-Jul-26	26-Jul-26 A	26-Jul-26 A	134,788.44	134,788.44	134,788.44	100%	100%
DAM3-P-DL-EN-120	HDPE pipes for water supply system	7	23-Jun-26	30-Jun-26	17-Aug-26 A	17-Aug-26 A	10,655.04	10,655.04	10,655.04	100%	100%
DAM3-P-DL-EN-160	Gate valve	7	16-Jul-26	23-Jul-26	05-Sep-26 A	20-Sep-26 A	42,658.36	42,658.36	42,658.36	100%	100%
DAM3-P-DL-EN-110	Directly buried gate valve for fire system	7	17-Jun-26	24-Jun-26	20-Sep-26 A	20-Sep-26 A	7,270.01	7,270.01	7,270.01	100%	100%
DAM3-P-DL-EN-130	Directly buried gate valve for water system	7	29-Jun-26	06-Jul-26	20-Sep-26 A	20-Sep-26 A	16,098.52	16,098.52	16,098.52	100%	100%
DAM3-P-DL-EN-140	Air valve	7	05-Jul-26	12-Jul-26	20-Sep-26 A	20-Sep-26 A	13,087.07	13,087.07	13,087.07	100%	100%
DAM3-P-DL-EN-150	Washout valve	7	11-Jul-26	18-Jul-26	20-Sep-26 A	20-Sep-26 A	15,346.94	15,346.94	15,346.94	100%	100%
STAGING TIME		107	20-Jun-26	06-Aug-26	25-Jul-26 A	20-Sep-26 A	0.00	0.00	0.00	0%	0%
DAM3-P-ST-EN-100	HDPE pipes for fire system	7	20-Jun-26	27-Jun-26	25-Jul-26 A	26-Jul-26 A	0.00	0.00	0.00	100%	100%
DAM3-P-ST-EN-170	UPVC pipes	7	30-Jul-26	06-Aug-26	26-Jul-26 A	26-Jul-26 A	0.00	0.00	0.00	100%	100%
DAM3-P-ST-EN-120	HDPE pipes for water supply system	7	01-Jul-26	08-Jul-26	17-Aug-26 A	17-Aug-26 A	0.00	0.00	0.00	100%	100%
DAM3-P-ST-EN-160	Gate valve	7	25-Jul-26	01-Aug-26	05-Sep-26 A	20-Sep-26 A	0.00	0.00	0.00	100%	100%
DAM3-P-ST-EN-110	Directly buried gate valve for fire system	7	25-Jun-26	02-Jul-26	20-Sep-26 A	20-Sep-26 A	0.00	0.00	0.00	100%	100%

2026 2027

Asphalt work
Interlock t
Curbstone
Gravel be
Road sign
Concrete
Road ma
21-Sep-2
Asphalt work
Interlock t
Curbstone
Gravel be
Road sign
Concrete
Road ma
20-Sep-2
21-Jun-26 A
HDPE pipes
Directly bure
HDPE pipes
Directly bure
Air valve
Washout val
Gate valve
UPVC pipes
19-Sep-2
HDPE pipe
Directly bu
Air valve
Washout v
Gate valve
UPVC pipes
HDPE pipes
Directly bu
20-Sep-2
HDPE pipes
UPVC pipes
HDPE pipe
Gate valve
Directly bu
Directly bu
Air valve
Washout
20-Sep-2
HDPE pipes
UPVC pipes
HDPE pipe
Gate valve
Directly bu

Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary

Date	Revision	Checked	Approved
06-Oct-26	Weekly Report		

Activity ID	Activity Name	Original Duration	BL Project Start	BL Project Finish	Start	Finish	Budgeted Total Cost	Planned Value Cost	Earned Value Cost	Schedule % Complete	Performance % Complete
DAM3-P-ST-EN-130	Directly buried gate valve for water system	7	07-Jul-26	14-Jul-26	20-Sep-26 A	20-Sep-26 A	0.00	0.00	0.00	100%	100%
DAM3-P-ST-EN-140	Air valve	7	13-Jul-26	20-Jul-26	20-Sep-26 A	20-Sep-26 A	0.00	0.00	0.00	100%	100%
DAM3-P-ST-EN-150	Washout valve	7	19-Jul-26	26-Jul-26	20-Sep-26 A	20-Sep-26 A	0.00	0.00	0.00	100%	100%
CONSTRUCTION (67%)		321	27-Jan-26	21-Feb-27	14-Jan-26 A	28-Feb-27	64,317,671.75	37,523,725.44	36,378,528.97	58.34%	56.56%
RBF 900 SQM FACTORIES		321	27-Jan-26	16-Feb-27	14-Jan-26 A	28-Feb-27	55,841,646.40	35,883,887.59	33,844,973.57	64.26%	60.61%
SITE WORKS		16	27-Jan-26	25-Feb-26	14-Jan-26 A	31-Jan-26 A	10,892.39	10,892.39	10,892.39	100%	100%
DAM3-C-GEN-88	Demolition of the existing pavement	12	10-Feb-26	25-Feb-26	14-Jan-26 A	31-Jan-26 A	10,892.39	10,892.39	10,892.39	100%	100%
DAM3-C-GEN-10	Initial Site Survey and Setting out	12	27-Jan-26	09-Feb-26	19-Jan-26 A	24-Jan-26 A	0.00	0.00	0.00	100%	100%
BLOCK B6		270	10-Feb-26	23-Nov-26	15-Feb-26 A	24-Jan-27	5,075,523.09	3,607,961.04	2,621,371.68	71.09%	51.65%
STRUCTURAL		196	10-Feb-26	07-Jul-26	15-Feb-26 A	29-Oct-26	1,389,042.53	1,389,042.53	1,388,135.41	100%	99.93%
FOOTING		74	10-Feb-26	25-Mar-26	15-Feb-26 A	10-May-26 A	597,655.16	597,655.16	597,655.16	100%	100%
DAM3-C-B6-S-160	Excavation for footings	8	10-Feb-26	19-Feb-26	15-Feb-26 A	24-Mar-26 A	89,859.61	89,859.61	89,859.61	100%	100%
DAM3-C-B6-S-6143	Soil replacement - rock fill	6	19-Feb-26	28-Feb-26	02-Apr-26 A	04-Apr-26 A	179,061.91	179,061.91	179,061.91	100%	100%
DAM3-C-B6-S-6153	Engineering fill	6	01-Mar-26	07-Mar-26	12-Apr-26 A	13-Apr-26 A	46,046.19	46,046.19	46,046.19	100%	100%
DAM3-C-B6-S-537	Lean Concrete Below Footings	2	10-Mar-26	11-Mar-26	22-Apr-26 A	22-Apr-26 A	8,229.34	8,229.34	8,229.34	100%	100%
DAM3-C-B6-S-687	Vapour Barrier for Footings	1	09-Mar-26	09-Mar-26	22-Apr-26 A	22-Apr-26 A	7,940.10	7,940.10	7,940.10	100%	100%
DAM3-C-B6-S-777	Anti Termite Below Footings	1	08-Mar-26	08-Mar-26	22-Apr-26 A	22-Apr-26 A	11,905.55	11,905.55	11,905.55	100%	100%
DAM3-C-B6-S-587	Rebar for Footings	4	12-Mar-26	16-Mar-26	02-May-26 A	05-May-26 A	101,844.98	101,844.98	101,844.98	100%	100%
DAM3-C-B6-S-597	Formwork for Footings	4	21-Mar-26	24-Mar-26	04-May-26 A	09-May-26 A	25,461.25	25,461.25	25,461.25	100%	100%
DAM3-C-B6-S-547	Pouring Concrete for Footings	1	25-Mar-26	25-Mar-26	10-May-26 A	10-May-26 A	127,306.23	127,306.23	127,306.23	100%	100%
COLUMN NECK		12	26-Mar-26	11-Apr-26	05-May-26 A	01-Jun-26 A	120,554.54	120,554.54	120,554.54	100%	100%
DAM3-C-B6-S-637	Rebar for column neck	2	26-Mar-26	28-Mar-26	05-May-26 A	09-May-26 A	14,919.19	14,919.19	14,919.19	100%	100%
DAM3-C-B6-S-647	Formwork for column neck	2	29-Mar-26	30-Mar-26	12-May-26 A	16-May-26 A	9,946.13	9,946.13	9,946.13	100%	100%
DAM3-C-B6-S-627	Pouring Concrete for column neck	1	31-Mar-26	31-Mar-26	17-May-26 A	17-May-26 A	24,865.31	24,865.31	24,865.31	100%	100%
DAM3-C-B6-S-677	Damp proof /Bitumin paint on Footings & column neck	2	01-Apr-26	02-Apr-26	18-May-26 A	19-May-26 A	24,777.73	24,777.73	24,777.73	100%	100%
DAM3-C-B6-S-737	Backfilling / Compaction up to Bottom of Grade Beams	7	04-Apr-26	11-Apr-26	24-May-26 A	01-Jun-26 A	46,046.19	46,046.19	46,046.19	100%	100%
GRADE BEAM		17	12-Apr-26	28-Apr-26	04-Jun-26 A	22-Jun-26 A	171,632.86	171,632.86	171,632.86	100%	100%
DAM3-C-B6-S-557	Lean Concrete Below Grade Beams	2	15-Apr-26	16-Apr-26	04-Jun-26 A	04-Jun-26 A	4,431.19	4,431.19	4,431.19	100%	100%
DAM3-C-B6-S-707	Vapour barrier for Grade Beams	2	13-Apr-26	14-Apr-26	04-Jun-26 A	04-Jun-26 A	5,293.40	5,293.40	5,293.40	100%	100%
DAM3-C-B6-S-787	Anti Termite Below Grade Beams	1	12-Apr-26	12-Apr-26	04-Jun-26 A	04-Jun-26 A	11,905.55	11,905.55	11,905.55	100%	100%
DAM3-C-B6-S-607	Rebar for Grade Beams	5	18-Apr-26	22-Apr-26	08-Jun-26 A	09-Jun-26 A	27,194.46	27,194.46	27,194.46	100%	100%
DAM3-C-B6-S-617	Formwork for Grade Beams	2	23-Apr-26	25-Apr-26	10-Jun-26 A	14-Jun-26 A	6,798.61	6,798.61	6,798.61	100%	100%
DAM3-C-B6-S-767	Anchor bolts installation	2	23-Apr-26	25-Apr-26	11-Jun-26 A	13-Jun-26 A	57,238.83	57,238.83	57,238.83	100%	100%
DAM3-C-B6-S-567	Pouring Concrete for Grade Beams	1	26-Apr-26	26-Apr-26	15-Jun-26 A	15-Jun-26 A	33,993.09	33,993.09	33,993.09	100%	100%
DAM3-C-B6-S-717	Damp proof /Bitumin paint on Grade Beams	2	27-Apr-26	28-Apr-26	20-Jun-26 A	22-Jun-26 A	24,777.73	24,777.73	24,777.73	100%	100%
SLAB ON GRADE		95	29-Apr-26	07-Jul-26	28-Jun-26 A	29-Oct-26	397,232.98	397,232.98	396,325.87	100%	99.77%
DAM3-C-B6-S-747	Backfilling / Compaction for Slab on Grade	7	29-Apr-26	06-May-26	28-Jun-26 A	06-Jul-26 A	23,023.09	23,023.09	23,023.09	100%	100%
DAM3-C-B6-S-577	Pouring Concrete for Ground Slab	4	11-May-26	14-May-26	18-Aug-26 A	23-Aug-26 A	344,195.21	344,195.21	344,195.21	100%	100%
DAM3-C-B6-S-697	Anti Termite Treatment below Ground Slab	1	07-May-26	07-May-26	18-Aug-26 A	23-Aug-26 A	15,874.08	15,874.08	15,874.08	100%	100%
DAM3-C-B6-S-727	Vapour barrier for below Ground Slab	2	09-May-26	10-May-26	18-Aug-26 A	23-Aug-26 A	13,233.49	13,233.49	13,233.49	100%	100%
DAM3-C-B6-S-757	Concrete pad	7	30-Jun-26	07-Jul-26	22-Oct-26	29-Oct-26	907.11	907.11	0.00	100%	0%
COLUMNS & BEAMS		65	07-May-26	07-Jun-26	08-Jun-26 A	06-Oct-26 A	101,966.98	101,966.98	101,966.98	100%	100%
DAM3-C-B6-S-6101	Rebar for Tie Beams	4	19-May-26	23-May-26	08-Jun-26 A	13-Jun-26 A	7,263.64	7,263.64	7,263.64	100%	100%
DAM3-C-B6-S-6102	Formwork for Tie Beams	2	24-May-26	25-May-26	11-Jun-26 A	14-Jun-26 A	1,815.91	1,815.91	1,815.91	100%	100%
DAM3-C-B6-S-6103	Pouring Concrete for Tie Beams	1	30-May-26	30-May-26	15-Jun-26 A	15-Jun-26 A	9,079.54	9,079.54	9,079.54	100%	100%
DAM3-C-B6-S-5101	Rebar for column	5	07-May-26	12-May-26	18-Jul-26 A	20-Jul-26 A	20,144.05	20,144.05	20,144.05	100%	100%
DAM3-C-B6-S-5102	Formwork for column	4	13-May-26	17-May-26	23-Jul-26 A	11-Aug-26 A	5,036.01	5,036.01	5,036.01	100%	100%
DAM3-C-B6-S-5103	Pouring Concrete for column	1	18-May-26	18-May-26	26-Jul-26 A	13-Aug-26 A	25,180.06	25,180.06	25,180.06	100%	100%
DAM3-C-B6-S-6113	Rebar for Beams	4	31-May-26	03-Jun-26	21-Sep-26 A	22-Sep-26 A	13,379.11	13,379.11	13,379.11	100%	100%

Activity ID	Activity Name	Original Duration	BL Project Start	BL Project Finish	Start	Finish	Budgeted Total Cost	Planned Value Cost	Earned Value Cost	Schedule % Complete	Performance % Complete
DAM3-C-B6-S-6123	Formwork for Beams	2	04-Jun-26	06-Jun-26	28-Sep-26 A	04-Oct-26 A	3,344.77	3,344.77	3,344.77	100%	100%
DAM3-C-B6-S-6133	Pouring Concrete for Beams	1	07-Jun-26	07-Jun-26	01-Oct-26 A	06-Oct-26 A	16,723.88	16,723.88	16,723.88	100%	100%
STRUCTURAL STEEL		77	16-May-26	12-Jul-26	06-Jul-26 A	27-Oct-26	1,566,668.48	1,566,668.48	1,097,706.76	100%	70.07%
DAM3-C-B6-SS-150	Installation of columns	3	16-May-26	18-May-26	06-Jul-26 A	06-Jul-26 A	217,507.55	217,507.55	217,507.55	100%	100%
DAM3-C-B6-SS-160	Installation of raft and purlins	5	19-May-26	24-May-26	06-Jul-26 A	07-Jul-26 A	326,261.32	326,261.32	326,261.32	100%	100%
DAM3-C-B6-SS-1020	Intumescent paint to steel works	7	25-May-26	04-Jun-26	25-Jul-26 A	17-Aug-26 A	317,759.56	317,759.56	317,759.56	100%	100%
DAM3-C-B6-SS-190	Installation of roof sheet	5	07-Jul-26	12-Jul-26	24-Aug-26 A	30-Aug-26 A	217,507.55	217,507.55	217,507.55	100%	100%
DAM3-C-B6-SS-1050	Steel members for external platform	7	08-Jun-26	15-Jun-26	30-Aug-26 A	31-Aug-26 A	18,670.78	18,670.78	18,670.78	100%	100%
DAM3-C-B6-SS-1030	Steel members for office area	7	25-May-26	04-Jun-26	06-Oct-26	13-Oct-26	115,805.20	115,805.20	0.00	100%	0%
DAM3-C-B6-SS-1040	Epoxy paint to steel members at office area	7	06-Jun-26	13-Jun-26	14-Oct-26	21-Oct-26	23,161.04	23,161.04	0.00	100%	0%
DAM3-C-B6-SS-1060	Epoxy paint for external platform	5	16-Jun-26	21-Jun-26	14-Oct-26	19-Oct-26	3,734.16	3,734.16	0.00	100%	0%
DAM3-C-B6-SS-180	Installation of wall sandwich panel	5	30-Jun-26	05-Jul-26	22-Oct-26	27-Oct-26	326,261.32	326,261.32	0.00	100%	0%
ARCHITECTURAL		102	25-May-26	03-Nov-26	15-Aug-26 A	07-Jan-27	900,244.66	550,323.72	85,409.37	61.13%	9.49%
MASONARY WORKS		35	25-May-26	07-Jul-26	29-Aug-26 A	15-Sep-26 A	78,954.21	78,954.21	78,954.21	100%	100%
DAM3-C-B6-A-170	Block work at factory area	10	25-May-26	08-Jun-26	29-Aug-26 A	07-Sep-26 A	58,338.72	58,338.72	58,338.72	100%	100%
DAM3-C-B6-A-200	Block work at office area	7	22-Jun-26	29-Jun-26	30-Aug-26 A	09-Sep-26 A	6,179.18	6,179.18	6,179.18	100%	100%
DAM3-C-B6-A-620	Block work at toilet area	7	30-Jun-26	07-Jul-26	31-Aug-26 A	15-Sep-26 A	14,436.31	14,436.31	14,436.31	100%	100%
WALL FINISHES		40	08-Jul-26	06-Oct-26	31-Oct-26	15-Dec-26	92,757.47	86,447.85	0.00	93.2%	0%
DAM3-C-B6-A-630	Internal Wall Plaster	15	08-Jul-26	25-Jul-26	31-Oct-26	16-Nov-26	48,590.16	48,590.16	0.00	100%	0%
DAM3-C-B6-A-680	Paint to Plaster (Primer, Putty & First Coat)	7	29-Sep-26	06-Oct-26	08-Dec-26	15-Dec-26	44,167.30	37,857.69	0.00	85.71%	0%
CIELING FINISHES		5	20-Sep-26	26-Sep-26	30-Nov-26	05-Dec-26	46,792.30	46,792.30	0.00	100%	0%
DAM3-C-B6-A-690	Installation of Ceiling Gypsum Board	5	20-Sep-26	26-Sep-26	30-Nov-26	05-Dec-26	46,792.30	46,792.30	0.00	100%	0%
FLOOR FINISHES		41	13-Aug-26	03-Nov-26	22-Nov-26	07-Jan-27	189,488.90	74,069.14	0.00	39.09%	0%
DAM3-C-B6-A-670	Tiles for Toilet	7	13-Aug-26	20-Aug-26	22-Nov-26	29-Nov-26	46,530.71	46,530.71	0.00	100%	0%
DAM3-C-B6-A-700	Tiles for Office Area	2	27-Sep-26	28-Sep-26	06-Dec-26	07-Dec-26	26,867.31	26,867.31	0.00	100%	0%
DAM3-C-B6-A-830	Granite strip	2	29-Sep-26	30-Sep-26	08-Dec-26	09-Dec-26	671.12	671.12	0.00	100%	0%
DAM3-C-B6-A-850	Epoxy paint	5	27-Oct-26	03-Nov-26	03-Jan-27	07-Jan-27	115,419.76	0.00	0.00	0%	0%
DOORS & WINDOWS		16	07-Jul-26	08-Aug-26	28-Oct-26	15-Nov-26	248,575.06	248,575.06	0.00	100%	0%
DAM3-C-B6-A-1010	Window (CW1)	7	07-Jul-26	14-Jul-26	28-Oct-26	04-Nov-26	94,173.21	94,173.21	0.00	100%	0%
DAM3-C-B6-A-640	Roll up Shutter Door	1	15-Jul-26	15-Jul-26	05-Nov-26	05-Nov-26	68,619.20	68,619.20	0.00	100%	0%
DAM3-C-B6-A-650	Supply and install (D5) 1000*2200mm single leaf steel door with door	1	16-Jul-26	16-Jul-26	07-Nov-26	07-Nov-26	16,016.16	16,016.16	0.00	100%	0%
DAM3-C-B6-A-710	Supply and install (D4) 800*2200 mm single leaf aluminum door with door	1	18-Jul-26	18-Jul-26	08-Nov-26	08-Nov-26	22,737.85	22,737.85	0.00	100%	0%
DAM3-C-B6-A-720	Supply and install (D7) 1000*2200 mm single leaf aluminum door with door	1	19-Jul-26	19-Jul-26	09-Nov-26	09-Nov-26	7,811.07	7,811.07	0.00	100%	0%
DAM3-C-B6-A-940	Supply and install (D3) 1000*2200 mm single leaf aluminum door with door	1	20-Jul-26	20-Jul-26	10-Nov-26	10-Nov-26	16,016.16	16,016.16	0.00	100%	0%
DAM3-C-B6-A-950	Supply and install fire rated 45 min (D2) 1200*2200 mm single leaf steel doo	1	30-Jul-26	30-Jul-26	11-Nov-26	11-Nov-26	16,711.52	16,711.52	0.00	100%	0%
DAM3-C-B6-A-960	Skylight fixtures installation	3	01-Aug-26	08-Aug-26	12-Nov-26	15-Nov-26	6,489.89	6,489.89	0.00	100%	0%
WATER PROOFING WORKS		4	09-Aug-26	12-Aug-26	17-Nov-26	21-Nov-26	4,879.02	4,879.02	0.00	100%	0%
DAM3-C-B6-A-810	Waterproofing membrane for toilets	4	09-Aug-26	12-Aug-26	17-Nov-26	21-Nov-26	4,879.02	4,879.02	0.00	100%	0%
METAL WORKS		22	01-Oct-26	15-Oct-26	15-Aug-26 A	22-Dec-26	193,717.06	10,606.15	6,455.16	5.48%	3.33%
DAM3-C-B6-A-750	Galvanised Steel Gratings	2	14-Oct-26	15-Oct-26	15-Aug-26 A	15-Aug-26 A	6,455.16	0.00	6,455.16	0%	100%
DAM3-C-B6-A-740	Steel Ladder	2	01-Oct-26	03-Oct-26	10-Dec-26	12-Dec-26	9,839.16	9,839.16	0.00	100%	0%
DAM3-C-B6-A-840	Steel railing works	4	04-Oct-26	07-Oct-26	13-Dec-26	16-Dec-26	1,533.98	766.99	0.00	50%	0%
DAM3-C-B6-A-760	Aluminium composite panel	5	08-Oct-26	13-Oct-26	17-Dec-26	22-Dec-26	175,888.76	0.00	0.00	0%	0%
SPECIALTIES		9	17-Oct-26	26-Oct-26	23-Dec-26	02-Jan-27	45,080.66	0.00	0.00	0%	0%
DAM3-C-B6-A-770	Installation of fittings	5	17-Oct-26	21-Oct-26	23-Dec-26	28-Dec-26	22,981.27	0.00	0.00	0%	0%
DAM3-C-B6-A-1000	Identification sign; ID01 & ID02	3	22-Oct-26	25-Oct-26	29-Dec-26	31-Dec-26	9,630.56	0.00	0.00	0%	0%
DAM3-C-B6-A-790	Furniture Installation	1	26-Oct-26	26-Oct-26	02-Jan-27	02-Jan-27	12,468.83	0.00	0.00	0%	0%
MECHANICAL		139	29-Apr-26	03-Nov-26	14-Jul-26 A	07-Jan-27	467,522.66	42,969.41	30,093.94	9.19%	6.44%
HVAC		17	15-Oct-26	31-Oct-26	16-Dec-26	04-Jan-27	233,183.33	0.00	0.00	0%	0%

Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary

Date	Revision	Checked	Approved
06-Oct-26	Weekly Report		

Activity ID	Activity Name	Original Duration	BL Project Start	BL Project Finish	Start	Finish	Budgeted Total Cost	Planned Value Cost	Earned Value Cost	Schedule % Complete	Performance % Complete	2026	2027
FIRST STAGE		4	22-Oct-26	26-Oct-26	23-Dec-26	27-Dec-26	170,694.73	0.00	0.00	0%	0%		27-Dec
DAM3-C-B6-M-450	Installation of HVAC Ducts	2	22-Oct-26	24-Oct-26	23-Dec-26	24-Dec-26	149,489.33	0.00	0.00	0%	0%		Installa
DAM3-C-B6-M-480	Installation of Duct insulation	2	25-Oct-26	26-Oct-26	26-Dec-26	27-Dec-26	21,205.40	0.00	0.00	0%	0%		Installa
SECOND STAGE		17	15-Oct-26	31-Oct-26	16-Dec-26	04-Jan-27	62,488.60	0.00	0.00	0%	0%		04-Jan
DAM3-C-B6-M-440	Installation of Exhaust Fans	2	15-Oct-26	17-Oct-26	16-Dec-26	17-Dec-26	7,938.56	0.00	0.00	0%	0%		Installa
DAM3-C-B6-M-470	Installation of Wall Propeller Type Exhaust Fan	4	18-Oct-26	21-Oct-26	19-Dec-26	22-Dec-26	46,831.64	0.00	0.00	0%	0%		Installa
DAM3-C-B6-M-460	Installation of Diffuser	2	27-Oct-26	28-Oct-26	28-Dec-26	29-Dec-26	2,144.00	0.00	0.00	0%	0%		Installa
DAM3-C-B6-M-650	Supply, install, test and commission door grilles & exhaust louvers	2	29-Oct-26	31-Oct-26	03-Jan-27	04-Jan-27	5,574.40	0.00	0.00	0%	0%		Supply
FIRE FIGHTING SYSTEM		20	07-Oct-26	03-Nov-26	16-Dec-26	07-Jan-27	102,458.78	0.00	0.00	0%	0%		07-Jan
FIRST STAGE		12	07-Oct-26	20-Oct-26	16-Dec-26	29-Dec-26	84,594.16	0.00	0.00	0%	0%		29-Dec
DAM3-C-B6-M-610	Installation of Fire Fighting Pipes (Seamless Black Steel)	7	07-Oct-26	14-Oct-26	16-Dec-26	23-Dec-26	72,394.75	0.00	0.00	0%	0%		Installa
DAM3-C-B6-M-620	Installation of Fire Fighting Valve	5	15-Oct-26	20-Oct-26	24-Dec-26	29-Dec-26	12,199.40	0.00	0.00	0%	0%		Installa
SECOND STAGE		8	21-Oct-26	03-Nov-26	30-Dec-26	07-Jan-27	17,864.62	0.00	0.00	0%	0%		07-Jan
DAM3-C-B6-M-630	Installation of Fire Hose Cabinet	3	21-Oct-26	24-Oct-26	30-Dec-26	02-Jan-27	15,158.56	0.00	0.00	0%	0%		Installa
DAM3-C-B6-M-680	Supply, install, test and commission Fire Department Connection(FDC)	3	01-Nov-26	03-Nov-26	05-Jan-27	07-Jan-27	2,706.06	0.00	0.00	0%	0%		Supply
SEWER AND DRAINAGE SYSTEM		121	29-Apr-26	27-Oct-26	14-Jul-26 A	17-Dec-26	90,009.74	42,969.41	30,093.94	47.74%	33.43%		17-Dec
FIRST STAGE		107	29-Apr-26	29-Aug-26	14-Jul-26 A	01-Dec-26	41,149.90	41,149.90	30,093.94	100%	73.13%		01-Dec
DAM3-C-B6-M-510	Installation of Sanitary Waste / Drainage Pipes	4	29-Apr-26	03-May-26	14-Jul-26 A	18-Jul-26 A	18,585.14	18,585.14	18,585.14	100%	100%		Installation
DAM3-C-B6-M-690	Installation of Trench drain	5	24-Aug-26	29-Aug-26	15-Jul-26 A	18-Jul-26 A	11,508.80	11,508.80	11,508.80	100%	100%		Installation
DAM3-C-B6-M-530	Installation of Floor Drain	2	22-Aug-26	23-Aug-26	30-Nov-26	01-Dec-26	11,055.96	11,055.96	0.00	100%	0%		Installat
SECOND STAGE		14	28-Sep-26	27-Oct-26	02-Dec-26	17-Dec-26	48,859.84	1,819.51	0.00	3.72%	0%		17-Dec
DAM3-C-B6-M-490	Installation of Electric Water Heater	2	28-Sep-26	29-Sep-26	02-Dec-26	03-Dec-26	1,819.51	1,819.51	0.00	100%	0%		Installat
DAM3-C-B6-M-500	Installation of Sanitary Fixture and Accessories	4	13-Oct-26	18-Oct-26	05-Dec-26	08-Dec-26	19,921.72	0.00	0.00	0%	0%		Installat
DAM3-C-B6-M-520	Installation of Lavotary /Wash Basin	2	18-Oct-26	20-Oct-26	09-Dec-26	10-Dec-26	21,416.68	0.00	0.00	0%	0%		Installat
DAM3-C-B6-M-580	Installation of Bib Tap	2	20-Oct-26	22-Oct-26	12-Dec-26	13-Dec-26	1,900.66	0.00	0.00	0%	0%		Installat
DAM3-C-B6-M-540	Installation of Water Tap	2	22-Oct-26	25-Oct-26	14-Dec-26	15-Dec-26	2,874.14	0.00	0.00	0%	0%		Installa
DAM3-C-B6-M-550	Installation of Roof Vent Cap	2	25-Oct-26	27-Oct-26	16-Dec-26	17-Dec-26	927.12	0.00	0.00	0%	0%		Installa
WATER SUPPLY SYSTEM		9	07-Oct-26	19-Oct-26	16-Dec-26	26-Dec-26	41,870.81	0.00	0.00	0%	0%		26-Dec
FIRST STAGE		6	07-Oct-26	13-Oct-26	16-Dec-26	22-Dec-26	41,592.68	0.00	0.00	0%	0%		22-Dec
DAM3-C-B6-M-600	Installation of Water Supply Pipes	4	07-Oct-26	11-Oct-26	16-Dec-26	20-Dec-26	23,318.41	0.00	0.00	0%	0%		Installa
DAM3-C-B6-M-590	Installation of Water Supply Valve	2	12-Oct-26	13-Oct-26	21-Dec-26	22-Dec-26	18,274.27	0.00	0.00	0%	0%		Installa
SECOND STAGE		3	14-Oct-26	19-Oct-26	23-Dec-26	26-Dec-26	278.13	0.00	0.00	0%	0%		26-Dec
DAM3-C-B6-M-640	Capped connection	3	14-Oct-26	19-Oct-26	23-Dec-26	26-Dec-26	278.13	0.00	0.00	0%	0%		Cappe
ELECTRICAL		172	20-May-26	23-Nov-26	08-Jun-26 A	24-Jan-27	752,044.76	58,956.90	20,026.20	7.84%	2.66%		24-Jan
FIRST STAGE		161	20-May-26	05-Nov-26	08-Jun-26 A	11-Jan-27	86,114.12	58,956.90	20,026.20	68.46%	23.26%		11-Jan
DAM3-C-B6-E-343	Installation of Earthing and Grounding	4	04-Jul-26	07-Jul-26	08-Jun-26 A	06-Oct-26	19,646.47	19,646.47	17,681.82	100%	90%		Installatio
DAM3-C-B6-E-413	Installation of Sleeves & Power outlet	8	20-May-26	01-Jun-26	08-Jun-26 A	10-Oct-26	2,920.45	2,920.45	1,460.23	100%	50%		Installatio
DAM3-C-B6-E-373	Installation of Conduits and wiring outlets - Fire Alarm System	4	14-Oct-26	18-Oct-26	09-Jun-26 A	24-Dec-26	1,768.31	0.00	884.15	0%	50%		Installa
DAM3-C-B6-E-453	Installation of LV Cables	4	21-Jul-26	25-Jul-26	06-Oct-26	10-Oct-26	36,389.98	36,389.98	0.00	100%	0%		Installatio
DAM3-C-B6-E-393	Installation of Conduites for Lighting Fixture	4	28-Oct-26	01-Nov-26	03-Jan-27	06-Jan-27	8,462.97	0.00	0.00	0%	0%		Installa
DAM3-C-B6-E-463	Installation of Wires	4	02-Nov-26	05-Nov-26	07-Jan-27	11-Jan-27	16,925.94	0.00	0.00	0%	0%		Installa
SECOND STAGE		95	07-Oct-26	23-Nov-26	06-Oct-26	24-Jan-27	665,930.64	0.00	0.00	0%	0%		24-Jan
DAM3-C-B6-E-730	Installation of Solar power plant	7	31-Oct-26	07-Nov-26	06-Oct-26	13-Oct-26	253,268.71	0.00	0.00	0%	0%		Installatio
DAM3-C-B6-E-503	Installation of Access Control System	4	28-Oct-26	01-Nov-26	06-Oct-26	10-Oct-26	27,616.86	0.00	0.00	0%	0%		Installatio
DAM3-C-B6-E-513	Monitor Modules for Fire Alarm	2	02-Nov-26	03-Nov-26	11-Oct-26	12-Oct-26	3,882.38	0.00	0.00	0%	0%		Monitor M
DAM3-C-B6-E-523	Line Isolator Modules for Fire Alarm	2	04-Nov-26	05-Nov-26	13-Oct-26	14-Oct-26	185.40	0.00	0.00	0%	0%		Line Isola
DAM3-C-B6-E-533	Firewarning flash light with sounder; wall mounted, Weather proof	2	04-Nov-26	05-Nov-26	13-Oct-26	14-Oct-26	3,082.69	0.00	0.00	0%	0%		Firewarni
DAM3-C-B6-E-403	Installation of Wiring Devices	4	07-Oct-26	11-Oct-26	16-Dec-26	20-Dec-26	19,435.09	0.00	0.00	0%	0%		Installa
DAM3-C-B6-E-433	Installation of Disconnect Switches	2	12-Oct-26	13-Oct-26	21-Dec-26	22-Dec-26	30,235.95	0.00	0.00	0%	0%		Installa

Date	Revision	Checked	Approved
06-Oct-26	Weekly Report		

Activity ID	Activity Name	Original Duration	BL Project Start	BL Project Finish	Start	Finish	Budgeted Total Cost	Planned Value Cost	Earned Value Cost	Schedule % Complete	Performance % Complete
DAM3-C-B6-E-353	Installation of Fire Alarm Control Panel	3	19-Oct-26	22-Oct-26	26-Dec-26	28-Dec-26	19,451.37	0.00	0.00	0%	0%
DAM3-C-B6-E-363	Installation of Fire Detectors & Accessories	4	24-Oct-26	27-Oct-26	29-Dec-26	02-Jan-27	56,740.37	0.00	0.00	0%	0%
DAM3-C-B6-E-383	Installation of Lighting fixtures	2	07-Nov-26	10-Nov-26	12-Jan-27	13-Jan-27	76,166.74	0.00	0.00	0%	0%
DAM3-C-B6-E-423	Installation of Main Distribution Board	2	11-Nov-26	12-Nov-26	14-Jan-27	16-Jan-27	32,472.73	0.00	0.00	0%	0%
DAM3-C-B6-E-473	Installation of LP-1 Panel	2	14-Nov-26	15-Nov-26	17-Jan-27	18-Jan-27	18,403.54	0.00	0.00	0%	0%
DAM3-C-B6-E-483	Installation of PP-AC panel	2	16-Nov-26	17-Nov-26	19-Jan-27	20-Jan-27	21,648.48	0.00	0.00	0%	0%
DAM3-C-B6-E-443	Installation of Telephone Cabinet	2	18-Nov-26	19-Nov-26	21-Jan-27	23-Jan-27	26,991.08	0.00	0.00	0%	0%
DAM3-C-B6-E-720	Installation of CCTV System	3	18-Nov-26	23-Nov-26	21-Jan-27	24-Jan-27	76,349.24	0.00	0.00	0%	0%
BLOCK B5		248	19-Feb-26	23-Nov-26	16-Feb-26 A	05-Jan-27	5,075,523.09	4,617,286.04	3,108,847.38	90.97%	61.25%
STRUCTURAL		176	19-Feb-26	25-Jul-26	16-Feb-26 A	13-Oct-26	1,389,042.53	1,389,042.53	1,388,135.41	100%	99.93%
FOOTING		44	19-Feb-26	25-Mar-26	16-Feb-26 A	05-May-26 A	597,655.16	597,655.16	597,655.16	100%	100%
DAM3-C-B5-S-250	Excavation for footings	4	19-Feb-26	25-Feb-26	16-Feb-26 A	18-Mar-26 A	89,859.61	89,859.61	89,859.61	100%	100%
DAM3-C-B5-S-6163	Soil replacement - rock fill	4	25-Feb-26	02-Mar-26	30-Mar-26 A	02-Apr-26 A	179,061.91	179,061.91	179,061.91	100%	100%
DAM3-C-B5-S-6173	Engineering fill	4	03-Mar-26	07-Mar-26	07-Apr-26 A	13-Apr-26 A	46,046.19	46,046.19	46,046.19	100%	100%
DAM3-C-B5-S-1057	Lean Concrete Below Footings	2	10-Mar-26	11-Mar-26	21-Apr-26 A	21-Apr-26 A	8,229.34	8,229.34	8,229.34	100%	100%
DAM3-C-B5-S-1207	Vapour Barrier for Footings	1	09-Mar-26	09-Mar-26	21-Apr-26 A	21-Apr-26 A	7,940.10	7,940.10	7,940.10	100%	100%
DAM3-C-B5-S-1297	Anti Termite Below Footings	1	08-Mar-26	08-Mar-26	21-Apr-26 A	21-Apr-26 A	11,905.55	11,905.55	11,905.55	100%	100%
DAM3-C-B5-S-1107	Rebar for Footings	4	12-Mar-26	16-Mar-26	28-Apr-26 A	29-Apr-26 A	101,844.98	101,844.98	101,844.98	100%	100%
DAM3-C-B5-S-1117	Formwork for Footings	4	21-Mar-26	24-Mar-26	02-May-26 A	03-May-26 A	25,461.25	25,461.25	25,461.25	100%	100%
DAM3-C-B5-S-1067	Pouring Concrete for Footings	1	25-Mar-26	25-Mar-26	05-May-26 A	05-May-26 A	127,306.23	127,306.23	127,306.23	100%	100%
COLUMN NECK		20	26-Mar-26	11-Apr-26	03-May-26 A	24-May-26 A	120,554.54	120,554.54	120,554.54	100%	100%
DAM3-C-B5-S-1157	Rebar for column neck	2	26-Mar-26	28-Mar-26	03-May-26 A	05-May-26 A	14,919.19	14,919.19	14,919.19	100%	100%
DAM3-C-B5-S-1167	Formwork for column neck	2	29-Mar-26	30-Mar-26	06-May-26 A	09-May-26 A	9,946.13	9,946.13	9,946.13	100%	100%
DAM3-C-B5-S-1147	Pouring Concrete for column neck	1	31-Mar-26	31-Mar-26	10-May-26 A	10-May-26 A	24,865.31	24,865.31	24,865.31	100%	100%
DAM3-C-B5-S-1197	Damp proof /Bitumin paint on Footings & column neck	2	01-Apr-26	02-Apr-26	11-May-26 A	12-May-26 A	24,777.73	24,777.73	24,777.73	100%	100%
DAM3-C-B5-S-1257	Backfilling / Compaction up to Bottom of Grade Beams	7	04-Apr-26	11-Apr-26	20-May-26 A	24-May-26 A	46,046.19	46,046.19	46,046.19	100%	100%
GRADE BEAM		13	12-Apr-26	28-Apr-26	01-Jun-26 A	18-Jun-26 A	171,632.86	171,632.86	171,632.86	100%	100%
DAM3-C-B5-S-1077	Lean Concrete Below Grade Beams	2	15-Apr-26	16-Apr-26	01-Jun-26 A	01-Jun-26 A	4,431.19	4,431.19	4,431.19	100%	100%
DAM3-C-B5-S-1227	Vapour barrier for Grade Beams	2	13-Apr-26	14-Apr-26	01-Jun-26 A	01-Jun-26 A	5,293.40	5,293.40	5,293.40	100%	100%
DAM3-C-B5-S-1307	Anti Termite Below Grade Beams	1	12-Apr-26	12-Apr-26	01-Jun-26 A	01-Jun-26 A	11,905.55	11,905.55	11,905.55	100%	100%
DAM3-C-B5-S-1287	Anchor bolts installation	2	23-Apr-26	25-Apr-26	02-Jun-26 A	04-Jun-26 A	57,238.83	57,238.83	57,238.83	100%	100%
DAM3-C-B5-S-1127	Rebar for Grade Beams	5	18-Apr-26	22-Apr-26	03-Jun-26 A	04-Jun-26 A	27,194.46	27,194.46	27,194.46	100%	100%
DAM3-C-B5-S-1137	Formwork for Grade Beams	2	23-Apr-26	25-Apr-26	03-Jun-26 A	07-Jun-26 A	6,798.61	6,798.61	6,798.61	100%	100%
DAM3-C-B5-S-1087	Pouring Concrete for Grade Beams	1	26-Apr-26	26-Apr-26	11-Jun-26 A	11-Jun-26 A	33,993.09	33,993.09	33,993.09	100%	100%
DAM3-C-B5-S-1237	Damp proof /Bitumin paint on Grade Beams	2	27-Apr-26	28-Apr-26	14-Jun-26 A	18-Jun-26 A	24,777.73	24,777.73	24,777.73	100%	100%
SLAB ON GRADE		97	29-Apr-26	29-Jun-26	21-Jun-26 A	13-Oct-26	397,232.98	397,232.98	396,325.87	100%	99.77%
DAM3-C-B5-S-1267	Backfilling / Compaction for Slab on Grade	7	29-Apr-26	06-May-26	21-Jun-26 A	24-Jun-26 A	23,023.09	23,023.09	23,023.09	100%	100%
DAM3-C-B5-S-1097	Pouring Concrete for Ground Slab	4	11-May-26	14-May-26	01-Aug-26 A	04-Aug-26 A	344,195.21	344,195.21	344,195.21	100%	100%
DAM3-C-B5-S-1217	Anti Termite Treatment below Ground Slab	1	07-May-26	07-May-26	01-Aug-26 A	04-Aug-26 A	15,874.08	15,874.08	15,874.08	100%	100%
DAM3-C-B5-S-1247	Vapour barrier for below Ground Slab	2	09-May-26	10-May-26	01-Aug-26 A	04-Aug-26 A	13,233.49	13,233.49	13,233.49	100%	100%
DAM3-C-B5-S-1277	Concrete pad	7	22-Jun-26	29-Jun-26	06-Oct-26	13-Oct-26	907.11	907.11	0.00	100%	0%
COLUMNS & BEAMS		77	07-May-26	25-Jul-26	03-Jun-26 A	22-Sep-26 A	101,966.98	101,966.98	101,966.98	100%	100%
DAM3-C-B5-S-6101	Rebar for Tie Beams	4	19-May-26	23-May-26	03-Jun-26 A	09-Jun-26 A	7,263.64	7,263.64	7,263.64	100%	100%
DAM3-C-B5-S-6102	Formwork for Tie Beams	2	24-May-26	25-May-26	04-Jun-26 A	10-Jun-26 A	1,815.91	1,815.91	1,815.91	100%	100%
DAM3-C-B5-S-6103	Pouring Concrete for Tie Beams	1	30-May-26	30-May-26	11-Jun-26 A	11-Jun-26 A	9,079.54	9,079.54	9,079.54	100%	100%
DAM3-C-B5-S-5101	Rebar for column	5	07-May-26	12-May-26	14-Jul-26 A	16-Jul-26 A	20,144.05	20,144.05	20,144.05	100%	100%
DAM3-C-B5-S-5102	Formwork for column	4	13-May-26	17-May-26	16-Jul-26 A	20-Jul-26 A	5,036.01	5,036.01	5,036.01	100%	100%
DAM3-C-B5-S-5103	Pouring Concrete for column	1	18-May-26	18-May-26	18-Jul-26 A	21-Jul-26 A	25,180.06	25,180.06	25,180.06	100%	100%
DAM3-C-B5-S-6113	Rebar for Beams	4	16-Jul-26	21-Jul-26	07-Sep-26 A	15-Sep-26 A	13,379.11	13,379.11	13,379.11	100%	100%

Activity ID	Activity Name	Original Duration	BL Project Start	BL Project Finish	Start	Finish	Budgeted Total Cost	Planned Value Cost	Earned Value Cost	Schedule % Complete	Performance % Complete
DAM3-C-B5-S-6123	Formwork for Beams	2	21-Jul-26	23-Jul-26	15-Sep-26 A	20-Sep-26 A	3,344.77	3,344.77	3,344.77	100%	100%
DAM3-C-B5-S-6133	Pouring Concrete for Beams	1	23-Jul-26	25-Jul-26	17-Sep-26 A	22-Sep-26 A	16,723.88	16,723.88	16,723.88	100%	100%
STRUCTURAL STEEL		83	16-May-26	30-Jul-26	02-Jul-26 A	13-Oct-26	1,566,668.48	1,566,668.48	1,507,147.15	100%	96.2%
DAM3-C-B5-SS-270	Installation of columns	3	16-May-26	18-May-26	02-Jul-26 A	05-Jul-26 A	217,507.55	217,507.55	217,507.55	100%	100%
DAM3-C-B5-SS-280	Installation of raft and purlins	5	19-May-26	24-May-26	02-Jul-26 A	06-Jul-26 A	326,261.32	326,261.32	326,261.32	100%	100%
DAM3-C-B5-SS-1840	Intumescent paint to steel works	7	25-May-26	04-Jun-26	12-Jul-26 A	20-Jul-26 A	317,759.56	317,759.56	317,759.56	100%	100%
DAM3-C-B5-SS-310	Installation of roof sheet	5	25-Jul-26	30-Jul-26	29-Jul-26 A	08-Aug-26 A	217,507.55	217,507.55	217,507.55	100%	100%
DAM3-C-B5-SS-1030	Steel members for external platform	7	14-Jun-26	21-Jun-26	31-Aug-26 A	01-Sep-26 A	18,670.78	18,670.78	18,670.78	100%	100%
DAM3-C-B5-SS-300	Installation of wall sandwich panel	5	22-Jun-26	27-Jun-26	04-Oct-26 A	06-Oct-26	326,261.32	326,261.32	293,635.19	100%	90%
DAM3-C-B5-SS-1850	Steel members for office area	7	06-Jun-26	13-Jun-26	05-Oct-26 A	06-Oct-26 A	115,805.20	115,805.20	115,805.20	100%	100%
DAM3-C-B5-SS-1020	Epoxy paint to steel members at office area	7	14-Jun-26	21-Jun-26	06-Oct-26	13-Oct-26	23,161.04	23,161.04	0.00	100%	0%
DAM3-C-B5-SS-1040	Epoxy paint for external platform	5	22-Jun-26	27-Jun-26	06-Oct-26	11-Oct-26	3,734.16	3,734.16	0.00	100%	0%
ARCHITECTURAL		102	25-May-26	21-Sep-26	08-Aug-26 A	08-Dec-26	900,244.66	900,244.66	121,851.99	100%	13.54%
MASONARY WORKS		26	25-May-26	29-Jun-26	09-Aug-26 A	09-Sep-26 A	78,954.21	78,954.21	78,954.21	100%	100%
DAM3-C-B5-A-290	Block work at factory area	10	25-May-26	08-Jun-26	09-Aug-26 A	12-Aug-26 A	58,338.72	58,338.72	58,338.72	100%	100%
DAM3-C-B5-A-320	Block work at office area	7	14-Jun-26	21-Jun-26	13-Aug-26 A	09-Sep-26 A	6,179.18	6,179.18	6,179.18	100%	100%
DAM3-C-B5-A-1440	Block work at toilet area	7	22-Jun-26	29-Jun-26	15-Aug-26 A	09-Sep-26 A	14,436.31	14,436.31	14,436.31	100%	100%
WALL FINISHES		29	09-Jul-26	24-Aug-26	26-Sep-26 A	12-Nov-26	92,757.47	92,757.47	36,442.62	100%	39.29%
DAM3-C-B5-A-1450	Internal Wall Plaster	15	09-Jul-26	26-Jul-26	26-Sep-26 A	14-Oct-26	48,590.16	48,590.16	36,442.62	100%	75%
DAM3-C-B5-A-1500	Paint to Plaster (Primer, Putty & First Coat)	7	17-Aug-26	24-Aug-26	04-Nov-26	12-Nov-26	44,167.30	44,167.30	0.00	100%	0%
CIELING FINISHES		5	09-Aug-26	13-Aug-26	27-Oct-26	02-Nov-26	46,792.30	46,792.30	0.00	100%	0%
DAM3-C-B5-A-1510	Installation of Ceiling Gypsum Board	5	09-Aug-26	13-Aug-26	27-Oct-26	02-Nov-26	46,792.30	46,792.30	0.00	100%	0%
FLOOR FINISHES		43	01-Aug-26	21-Sep-26	19-Oct-26	08-Dec-26	189,488.90	189,488.90	0.00	100%	0%
DAM3-C-B5-A-1490	Tiles for Toilet	7	01-Aug-26	08-Aug-26	19-Oct-26	27-Oct-26	46,530.71	46,530.71	0.00	100%	0%
DAM3-C-B5-A-1520	Tiles for Office Area	2	15-Aug-26	16-Aug-26	02-Nov-26	04-Nov-26	26,867.31	26,867.31	0.00	100%	0%
DAM3-C-B5-A-1650	Granite strip	2	17-Aug-26	18-Aug-26	04-Nov-26	07-Nov-26	671.12	671.12	0.00	100%	0%
DAM3-C-B5-A-1670	Epoxy paint	7	14-Sep-26	21-Sep-26	30-Nov-26	08-Dec-26	115,419.76	115,419.76	0.00	100%	0%
DOORS & WINDOWS		14	28-Jun-26	13-Jul-26	06-Oct-26	22-Oct-26	248,575.06	248,575.06	0.00	100%	0%
DAM3-C-B5-A-1830	Window (CW1)	7	28-Jun-26	05-Jul-26	06-Oct-26	14-Oct-26	94,173.21	94,173.21	0.00	100%	0%
DAM3-C-B5-A-1460	Roll up Shutter Door	1	06-Jul-26	06-Jul-26	14-Oct-26	15-Oct-26	68,619.20	68,619.20	0.00	100%	0%
DAM3-C-B5-A-1470	Supply and install (D5) 1000*2200mm single leaf steel door with door	1	07-Jul-26	07-Jul-26	15-Oct-26	17-Oct-26	16,016.16	16,016.16	0.00	100%	0%
DAM3-C-B5-A-1530	Supply and install (D4) 800*2200 mm single leaf aluminum door with door	1	08-Jul-26	08-Jul-26	17-Oct-26	18-Oct-26	22,737.85	22,737.85	0.00	100%	0%
DAM3-C-B5-A-1540	Supply and install (D7) 1000*2200 mm single leaf aluminum door with door	1	09-Jul-26	09-Jul-26	18-Oct-26	19-Oct-26	7,811.07	7,811.07	0.00	100%	0%
DAM3-C-B5-A-1760	Supply and install (D3) 1000*2200 mm single leaf aluminum door with door	1	11-Jul-26	11-Jul-26	19-Oct-26	20-Oct-26	16,016.16	16,016.16	0.00	100%	0%
DAM3-C-B5-A-1770	Supply and install fire rated 45 min (D2) 1200*2200 mm single leaf steel doo	1	12-Jul-26	12-Jul-26	20-Oct-26	21-Oct-26	16,711.52	16,711.52	0.00	100%	0%
DAM3-C-B5-A-1780	Skylight fixtures installation	1	13-Jul-26	13-Jul-26	21-Oct-26	22-Oct-26	6,489.89	6,489.89	0.00	100%	0%
WATER PROOFING WORKS		4	27-Jul-26	30-Jul-26	14-Oct-26	19-Oct-26	4,879.02	4,879.02	0.00	100%	0%
DAM3-C-B5-A-1630	Waterproofing membrane for toilets	4	27-Jul-26	30-Jul-26	14-Oct-26	19-Oct-26	4,879.02	4,879.02	0.00	100%	0%
METAL WORKS		18	19-Aug-26	02-Sep-26	08-Aug-26 A	19-Nov-26	193,717.06	193,717.06	6,455.16	100%	3.33%
DAM3-C-B5-A-1570	Galvanised Steel Gratings	2	01-Sep-26	02-Sep-26	08-Aug-26 A	08-Aug-26 A	6,455.16	6,455.16	6,455.16	100%	100%
DAM3-C-B5-A-1560	Steel Ladder	2	19-Aug-26	20-Aug-26	07-Nov-26	09-Nov-26	9,839.16	9,839.16	0.00	100%	0%
DAM3-C-B5-A-1660	Steel railing works	4	22-Aug-26	25-Aug-26	09-Nov-26	14-Nov-26	1,533.98	1,533.98	0.00	100%	0%
DAM3-C-B5-A-1580	Aluminium composite panel	5	26-Aug-26	31-Aug-26	14-Nov-26	19-Nov-26	175,888.76	175,888.76	0.00	100%	0%
SPECIALTIES		9	03-Sep-26	13-Sep-26	19-Nov-26	30-Nov-26	45,080.66	45,080.66	0.00	100%	0%
DAM3-C-B5-A-1590	Installation of fittings	5	03-Sep-26	08-Sep-26	19-Nov-26	25-Nov-26	22,981.27	22,981.27	0.00	100%	0%
DAM3-C-B5-A-1820	Identification sign; ID01 & ID02	3	09-Sep-26	12-Sep-26	25-Nov-26	29-Nov-26	9,630.56	9,630.56	0.00	100%	0%
DAM3-C-B5-A-1610	Furniture Installation	1	13-Sep-26	13-Sep-26	29-Nov-26	30-Nov-26	12,468.83	12,468.83	0.00	100%	0%
MECHANICAL		119	29-Apr-26	13-Sep-26	08-Jul-26 A	02-Dec-26	467,522.66	467,522.66	71,686.63	100%	15.33%
HVAC		14	25-Aug-26	09-Sep-26	12-Nov-26	29-Nov-26	233,183.33	233,183.33	0.00	100%	0%

2026 2027

Actual Level of Effort | Remaining Work | Milestone
Actual Work | Critical Remaining Work | summary

Date	Revision	Checked	Approved
06-Oct-26	Weekly Report		

Activity ID	Activity Name	Original Duration	BL Project Start	BL Project Finish	Start	Finish	Budgeted Total Cost	Planned Value Cost	Earned Value Cost	Schedule % Complete	Performance % Complete
FIRST STAGE		4	01-Sep-26	05-Sep-26	19-Nov-26	24-Nov-26	170,694.73	170,694.73	0.00	100%	0%
DAM3-C-B5-M-1070	Installation of HVAC Ducts	2	01-Sep-26	02-Sep-26	19-Nov-26	22-Nov-26	149,489.33	149,489.33	0.00	100%	0%
DAM3-C-B5-M-1100	Installation of Duct insulation	2	03-Sep-26	05-Sep-26	22-Nov-26	24-Nov-26	21,205.40	21,205.40	0.00	100%	0%
SECOND STAGE		14	25-Aug-26	09-Sep-26	12-Nov-26	29-Nov-26	62,488.60	62,488.60	0.00	100%	0%
DAM3-C-B5-M-1060	Installation of Exhaust Fans	2	25-Aug-26	26-Aug-26	12-Nov-26	15-Nov-26	7,938.56	7,938.56	0.00	100%	0%
DAM3-C-B5-M-1090	Installation of Wall Propeller Type Exhaust Fan	4	27-Aug-26	31-Aug-26	15-Nov-26	19-Nov-26	46,831.64	46,831.64	0.00	100%	0%
DAM3-C-B5-M-1080	Installation of Diffuser	2	06-Sep-26	07-Sep-26	24-Nov-26	26-Nov-26	2,144.00	2,144.00	0.00	100%	0%
DAM3-C-B5-M-1270	Supply, install, test and commission door grilles & exhaust louvers	2	08-Sep-26	09-Sep-26	26-Nov-26	29-Nov-26	5,574.40	5,574.40	0.00	100%	0%
FIRE FIGHTING SYSTEM		17	25-Aug-26	13-Sep-26	12-Nov-26	02-Dec-26	102,458.78	102,458.78	0.00	100%	0%
FIRST STAGE		12	25-Aug-26	07-Sep-26	12-Nov-26	26-Nov-26	84,594.16	84,594.16	0.00	100%	0%
DAM3-C-B5-M-1230	Installation of Fire Fighting Pipes (Seamless Black Steel)	7	25-Aug-26	01-Sep-26	12-Nov-26	21-Nov-26	72,394.75	72,394.75	0.00	100%	0%
DAM3-C-B5-M-1240	Installation of Fire Fighting Valve	5	02-Sep-26	07-Sep-26	21-Nov-26	26-Nov-26	12,199.40	12,199.40	0.00	100%	0%
SECOND STAGE		5	08-Sep-26	13-Sep-26	26-Nov-26	02-Dec-26	17,864.62	17,864.62	0.00	100%	0%
DAM3-C-B5-M-1250	Installation of Fire Hose Cabinet	3	08-Sep-26	10-Sep-26	26-Nov-26	30-Nov-26	15,158.56	15,158.56	0.00	100%	0%
DAM3-C-B5-M-1300	Supply, install, test and commission Fire Department Connection(FDC)	3	10-Sep-26	13-Sep-26	29-Nov-26	02-Dec-26	2,706.06	2,706.06	0.00	100%	0%
SEWER AND DRAINAGE SYSTEM		103	29-Apr-26	01-Sep-26	08-Jul-26 A	15-Nov-26	90,009.74	90,009.74	30,093.94	100%	33.43%
FIRST STAGE		89	29-Apr-26	16-Aug-26	08-Jul-26 A	29-Oct-26	41,149.90	41,149.90	30,093.94	100%	73.13%
DAM3-C-B5-M-1130	Installation of Sanitary Waste / Drainage Pipes	4	29-Apr-26	03-May-26	08-Jul-26 A	12-Jul-26 A	18,585.14	18,585.14	18,585.14	100%	100%
DAM3-C-B5-M-1310	Installation of Trench drain	5	11-Aug-26	16-Aug-26	11-Jul-26 A	14-Jul-26 A	11,508.80	11,508.80	11,508.80	100%	100%
DAM3-C-B5-M-1150	Installation of Floor Drain	2	09-Aug-26	10-Aug-26	27-Oct-26	29-Oct-26	11,055.96	11,055.96	0.00	100%	0%
SECOND STAGE		14	17-Aug-26	01-Sep-26	29-Oct-26	15-Nov-26	48,859.84	48,859.84	0.00	100%	0%
DAM3-C-B5-M-1110	Installation of Electric Water Heater	2	17-Aug-26	18-Aug-26	29-Oct-26	01-Nov-26	1,819.51	1,819.51	0.00	100%	0%
DAM3-C-B5-M-1120	Installation of Sanitary Fixture and Accessories	4	19-Aug-26	23-Aug-26	01-Nov-26	05-Nov-26	19,921.72	19,921.72	0.00	100%	0%
DAM3-C-B5-M-1140	Installation of Lavotary /Wash Basin	2	24-Aug-26	25-Aug-26	05-Nov-26	08-Nov-26	21,416.68	21,416.68	0.00	100%	0%
DAM3-C-B5-M-1200	Installation of Bib Tap	2	26-Aug-26	27-Aug-26	08-Nov-26	10-Nov-26	1,900.66	1,900.66	0.00	100%	0%
DAM3-C-B5-M-1160	Installation of Water Tap	2	29-Aug-26	30-Aug-26	10-Nov-26	12-Nov-26	2,874.14	2,874.14	0.00	100%	0%
DAM3-C-B5-M-1170	Installation of Roof Vent Cap	2	31-Aug-26	01-Sep-26	12-Nov-26	15-Nov-26	927.12	927.12	0.00	100%	0%
WATER SUPPLY SYSTEM		19	25-Aug-26	06-Sep-26	29-Sep-26 A	18-Nov-26	41,870.81	41,870.81	41,592.68	100%	99.34%
FIRST STAGE		6	25-Aug-26	31-Aug-26	29-Sep-26 A	03-Oct-26 A	41,592.68	41,592.68	41,592.68	100%	100%
DAM3-C-B5-M-1210	Installation of Water Supply Valve	2	30-Aug-26	31-Aug-26	29-Sep-26 A	03-Oct-26 A	18,274.27	18,274.27	18,274.27	100%	100%
DAM3-C-B5-M-1220	Installation of Water Supply Pipes	4	25-Aug-26	29-Aug-26	29-Sep-26 A	03-Oct-26 A	23,318.41	23,318.41	23,318.41	100%	100%
SECOND STAGE		5	01-Sep-26	06-Sep-26	12-Nov-26	18-Nov-26	278.13	278.13	0.00	100%	0%
DAM3-C-B5-M-1260	Capped connection	5	01-Sep-26	06-Sep-26	12-Nov-26	18-Nov-26	278.13	278.13	0.00	100%	0%
ELECTRICAL		124	30-Jun-26	23-Nov-26	04-Jun-26 A	05-Jan-27	752,044.76	293,807.71	20,026.20	39.07%	2.66%
FIRST STAGE		118	30-Jun-26	13-Oct-26	04-Jun-26 A	29-Dec-26	86,114.12	30,077.67	20,026.20	34.93%	23.26%
DAM3-C-B5-E-803	Installation of Earthing and Grounding	4	10-Oct-26	13-Oct-26	04-Jun-26 A	26-Dec-26	19,646.47	0.00	17,681.82	0%	90%
DAM3-C-B5-E-833	Installation of Conduits and wiring outlets - Fire Alarm System	4	01-Sep-26	05-Sep-26	04-Jun-26 A	22-Nov-26	1,768.31	1,768.31	884.15	100%	50%
DAM3-C-B5-E-873	Installation of Sleeves & Power outlet	8	30-Jun-26	08-Jul-26	04-Jun-26 A	10-Oct-26	2,920.45	2,920.45	1,460.23	100%	50%
DAM3-C-B5-E-853	Installation of Conduites for Lighting Fixture	4	15-Sep-26	19-Sep-26	01-Dec-26	06-Dec-26	8,462.97	8,462.97	0.00	100%	0%
DAM3-C-B5-E-923	Installation of Wires	4	20-Sep-26	24-Sep-26	06-Dec-26	10-Dec-26	16,925.94	16,925.94	0.00	100%	0%
DAM3-C-B5-E-913	Installation of LV Cables	4	10-Oct-26	13-Oct-26	24-Dec-26	29-Dec-26	36,389.98	0.00	0.00	0%	0%
SECOND STAGE		72	25-Aug-26	23-Nov-26	14-Oct-26	05-Jan-27	665,930.64	263,730.03	0.00	39.6%	0%
DAM3-C-B5-E-1350	Installation of Solar power plant	14	08-Nov-26	23-Nov-26	14-Oct-26	29-Oct-26	253,268.71	0.00	0.00	0%	0%
DAM3-C-B5-E-863	Installation of Wiring Devices	4	25-Aug-26	29-Aug-26	12-Nov-26	17-Nov-26	19,435.09	19,435.09	0.00	100%	0%
DAM3-C-B5-E-893	Installation of Disconnect Switches	2	30-Aug-26	31-Aug-26	17-Nov-26	19-Nov-26	30,235.95	30,235.95	0.00	100%	0%
DAM3-C-B5-E-813	Installation of Fire Alarm Control Panel	4	06-Sep-26	09-Sep-26	22-Nov-26	26-Nov-26	19,451.37	19,451.37	0.00	100%	0%
DAM3-C-B5-E-823	Installation of Fire Detectors & Accessories	4	10-Sep-26	14-Sep-26	26-Nov-26	01-Dec-26	56,740.37	56,740.37	0.00	100%	0%
DAM3-C-B5-E-843	Installation of Lighting fixtures	4	26-Sep-26	29-Sep-26	10-Dec-26	15-Dec-26	76,166.74	76,166.74	0.00	100%	0%
DAM3-C-B5-E-883	Installation of Main Distribution Board	2	30-Sep-26	01-Oct-26	15-Dec-26	17-Dec-26	32,472.73	32,472.73	0.00	100%	0%

Activity ID	Activity Name	Original Duration	BL Project Start	BL Project Finish	Start	Finish	Budgeted Total Cost	Planned Value Cost	Earned Value Cost	Schedule % Complete	Performance % Complete	2026	2027
DAM3-C-B5-E-933	Installation of LP-1 Panel	2	03-Oct-26	04-Oct-26	17-Dec-26	20-Dec-26	18,403.54	18,403.54	0.00	100%	0%	Installa	
DAM3-C-B5-E-943	Installation of PP-AC panel	2	05-Oct-26	06-Oct-26	20-Dec-26	22-Dec-26	21,648.48	10,824.24	0.00	50%	0%	Installa	
DAM3-C-B5-E-903	Installation of Telephone Cabinet	2	07-Oct-26	08-Oct-26	22-Dec-26	24-Dec-26	26,991.08	0.00	0.00	0%	0%	Installa	
DAM3-C-B5-E-1340	Installation of CCTV System	7	07-Oct-26	14-Oct-26	22-Dec-26	30-Dec-26	76,349.24	0.00	0.00	0%	0%	Installa	
DAM3-C-B5-E-963	Installation of Access Control System	4	10-Oct-26	13-Oct-26	24-Dec-26	29-Dec-26	27,616.86	0.00	0.00	0%	0%	Installa	
DAM3-C-B5-E-973	Monitor Modules for Fire Alarm	2	14-Oct-26	15-Oct-26	29-Dec-26	31-Dec-26	3,882.38	0.00	0.00	0%	0%	Monito	
DAM3-C-B5-E-983	Line Isolator Modules for Fire Alarm	2	17-Oct-26	18-Oct-26	31-Dec-26	03-Jan-27	185.40	0.00	0.00	0%	0%	Line Is	
DAM3-C-B5-E-993	Firewarning flash light with sounder; wall mounted, Weather proof	2	19-Oct-26	20-Oct-26	03-Jan-27	05-Jan-27	3,082.69	0.00	0.00	0%	0%	Firewa	
BLOCK B4		243	25-Feb-26	01-Dec-26	17-Feb-26 A	04-Jan-27	5,075,523.09	4,290,448.70	3,245,831.89	84.53%	63.95%	04-Jan	
STRUCTURAL		186	25-Feb-26	21-Jul-26	17-Feb-26 A	29-Oct-26	1,389,042.53	1,389,042.53	1,388,135.41	100%	99.93%	29-Oct-2	
FOOTING		36	25-Feb-26	30-Mar-26	17-Feb-26 A	30-Apr-26 A	597,655.16	597,655.16	597,655.16	100%	100%	30-Apr-26 A, F	
DAM3-C-B4-S-210	Excavation for footings	4	25-Feb-26	02-Mar-26	17-Feb-26 A	24-Mar-26 A	89,859.61	89,859.61	89,859.61	100%	100%	Excavation for	
DAM3-C-B4-S-6183	Soil replacement - rock fill	4	03-Mar-26	07-Mar-26	26-Mar-26 A	29-Mar-26 A	179,061.91	179,061.91	179,061.91	100%	100%	Soil replaceme	
DAM3-C-B4-S-6193	Engineering fill	4	08-Mar-26	11-Mar-26	02-Apr-26 A	05-Apr-26 A	46,046.19	46,046.19	46,046.19	100%	100%	Engineering fill	
DAM3-C-B4-S-797	Lean Concrete Below Footings	2	15-Mar-26	16-Mar-26	15-Apr-26 A	15-Apr-26 A	8,229.34	8,229.34	8,229.34	100%	100%	Lean Concrete	
DAM3-C-B4-S-947	Vapour Barrier for Footings	1	14-Mar-26	14-Mar-26	15-Apr-26 A	15-Apr-26 A	7,940.10	7,940.10	7,940.10	100%	100%	Vapour Barrier	
DAM3-C-B4-S-1037	Anti Termite Below Footings	1	12-Mar-26	12-Mar-26	15-Apr-26 A	15-Apr-26 A	11,905.55	11,905.55	11,905.55	100%	100%	Anti Termite Be	
DAM3-C-B4-S-857	Formwork for Footings	4	25-Mar-26	29-Mar-26	20-Apr-26 A	22-Apr-26 A	25,461.25	25,461.25	25,461.25	100%	100%	Formwork for F	
DAM3-C-B4-S-847	Rebar for Footings	4	21-Mar-26	24-Mar-26	23-Apr-26 A	28-Apr-26 A	101,844.98	101,844.98	101,844.98	100%	100%	Rebar for Foo	
DAM3-C-B4-S-807	Pouring Concrete for Footings	1	30-Mar-26	30-Mar-26	30-Apr-26 A	30-Apr-26 A	127,306.23	127,306.23	127,306.23	100%	100%	Pouring Concr	
COLUMN NECK		17	31-Mar-26	15-Apr-26	23-Apr-26 A	19-May-26 A	120,554.54	120,554.54	120,554.54	100%	100%	19-May-26 A,	
DAM3-C-B4-S-897	Rebar for column neck	2	31-Mar-26	01-Apr-26	23-Apr-26 A	28-Apr-26 A	14,919.19	14,919.19	14,919.19	100%	100%	Rebar for colu	
DAM3-C-B4-S-907	Formwork for column neck	2	02-Apr-26	04-Apr-26	03-May-26 A	05-May-26 A	9,946.13	9,946.13	9,946.13	100%	100%	Formwork for c	
DAM3-C-B4-S-887	Pouring Concrete for column neck	1	05-Apr-26	05-Apr-26	05-May-26 A	05-May-26 A	24,865.31	24,865.31	24,865.31	100%	100%	Pouring Concr	
DAM3-C-B4-S-937	Damp proof /Bitumin paint on Footings & column neck	2	06-Apr-26	07-Apr-26	07-May-26 A	10-May-26 A	24,777.73	24,777.73	24,777.73	100%	100%	Damp proof /B	
DAM3-C-B4-S-997	Backfilling / Compaction up to Bottom of Grade Beams	7	08-Apr-26	15-Apr-26	13-May-26 A	19-May-26 A	46,046.19	46,046.19	46,046.19	100%	100%	Backfilling / C	
GRADE BEAM		17	16-Apr-26	06-May-26	20-May-26 A	09-Jun-26 A	171,632.86	171,632.86	171,632.86	100%	100%	09-Jun-26 A,	
DAM3-C-B4-S-817	Lean Concrete Below Grade Beams	2	20-Apr-26	21-Apr-26	20-May-26 A	20-May-26 A	4,431.19	4,431.19	4,431.19	100%	100%	Lean Concret	
DAM3-C-B4-S-967	Vapour barrier for Grade Beams	2	18-Apr-26	19-Apr-26	20-May-26 A	20-May-26 A	5,293.40	5,293.40	5,293.40	100%	100%	Vapour barrie	
DAM3-C-B4-S-1047	Anti Termite Below Grade Beams	1	16-Apr-26	16-Apr-26	20-May-26 A	20-May-26 A	11,905.55	11,905.55	11,905.55	100%	100%	Anti Termite B	
DAM3-C-B4-S-867	Rebar for Grade Beams	5	22-Apr-26	27-Apr-26	21-May-26 A	24-May-26 A	27,194.46	27,194.46	27,194.46	100%	100%	Rebar for Gra	
DAM3-C-B4-S-877	Formwork for Grade Beams	2	28-Apr-26	29-Apr-26	24-May-26 A	02-Jun-26 A	6,798.61	6,798.61	6,798.61	100%	100%	Formwork for	
DAM3-C-B4-S-1027	Anchor bolts installation	2	28-Apr-26	29-Apr-26	31-May-26 A	01-Jun-26 A	57,238.83	57,238.83	57,238.83	100%	100%	Anchor bolts	
DAM3-C-B4-S-827	Pouring Concrete for Grade Beams	1	30-Apr-26	30-Apr-26	03-Jun-26 A	03-Jun-26 A	33,993.09	33,993.09	33,993.09	100%	100%	Pouring Conc	
DAM3-C-B4-S-977	Damp proof /Bitumin paint on Grade Beams	5	02-May-26	06-May-26	07-Jun-26 A	09-Jun-26 A	24,777.73	24,777.73	24,777.73	100%	100%	Damp proof /	
SLAB ON GRADE		116	07-May-26	21-Jul-26	14-Jun-26 A	29-Oct-26	397,232.98	397,232.98	396,325.87	100%	99.77%	29-Oct-2	
DAM3-C-B4-S-1007	Backfilling / Compaction for Slab on Grade	7	07-May-26	14-May-26	14-Jun-26 A	22-Jun-26 A	23,023.09	23,023.09	23,023.09	100%	100%	Backfilling / C	
DAM3-C-B4-S-837	Pouring Concrete for Ground Slab	4	19-May-26	23-May-26	29-Jul-26 A	01-Aug-26 A	344,195.21	344,195.21	344,195.21	100%	100%	Pouring Co	
DAM3-C-B4-S-957	Anti Termite Treatment below Ground Slab	1	16-May-26	16-May-26	29-Jul-26 A	01-Aug-26 A	15,874.08	15,874.08	15,874.08	100%	100%	Anti Termite	
DAM3-C-B4-S-987	Vapour barrier for below Ground Slab	2	17-May-26	18-May-26	29-Jul-26 A	01-Aug-26 A	13,233.49	13,233.49	13,233.49	100%	100%	Vapour bar	
DAM3-C-B4-S-1017	Concrete pad	7	14-Jul-26	21-Jul-26	22-Oct-26	29-Oct-26	907.11	907.11	0.00	100%	0%	Concrete	
COLUMNS & BEAMS		61	16-May-26	15-Jun-26	21-May-26 A	14-Sep-26 A	101,966.98	101,966.98	101,966.98	100%	100%	14-Sep-26	
DAM3-C-B4-S-6101	Rebar for Tie Beams	4	31-May-26	03-Jun-26	21-May-26 A	24-May-26 A	7,263.64	7,263.64	7,263.64	100%	100%	Rebar for Tie	
DAM3-C-B4-S-6102	Formwork for Tie Beams	2	04-Jun-26	06-Jun-26	24-May-26 A	02-Jun-26 A	1,815.91	1,815.91	1,815.91	100%	100%	Formwork for	
DAM3-C-B4-S-6103	Pouring Concrete for Tie Beams	1	07-Jun-26	07-Jun-26	03-Jun-26 A	03-Jun-26 A	9,079.54	9,079.54	9,079.54	100%	100%	Pouring Conc	
DAM3-C-B4-S-5101	Rebar for column	5	16-May-26	20-May-26	22-Jun-26 A	02-Jul-26 A	20,144.05	20,144.05	20,144.05	100%	100%	Rebar for co	
DAM3-C-B4-S-5102	Formwork for column	4	21-May-26	25-May-26	29-Jun-26 A	05-Jul-26 A	5,036.01	5,036.01	5,036.01	100%	100%	Formwork fo	
DAM3-C-B4-S-5103	Pouring Concrete for column	1	30-May-26	30-May-26	09-Jul-26 A	12-Jul-26 A	25,180.06	25,180.06	25,180.06	100%	100%	Pouring Co	
DAM3-C-B4-S-6113	Rebar for Beams	4	08-Jun-26	11-Jun-26	30-Aug-26 A	01-Sep-26 A	13,379.11	13,379.11	13,379.11	100%	100%	Rebar for	

Activity ID	Activity Name	Original Duration	BL Project Start	BL Project Finish	Start	Finish	Budgeted Total Cost	Planned Value Cost	Earned Value Cost	Schedule % Complete	Performance % Complete
DAM3-C-B4-S-6123	Formwork for Beams	2	13-Jun-26	14-Jun-26	02-Sep-26 A	08-Sep-26 A	3,344.77	3,344.77	3,344.77	100%	100%
DAM3-C-B4-S-6133	Pouring Concrete for Beams	1	15-Jun-26	15-Jun-26	08-Sep-26 A	14-Sep-26 A	16,723.88	16,723.88	16,723.88	100%	100%
STRUCTURAL STEEL		94	25-May-26	19-Jul-26	24-Jun-26 A	28-Oct-26	1,566,668.48	1,566,668.48	1,539,773.29	100%	98.28%
DAM3-C-B4-A-210	Installation of columns	3	25-May-26	31-May-26	24-Jun-26 A	24-Jun-26 A	217,507.55	217,507.55	217,507.55	100%	100%
DAM3-C-B4-A-220	Installation of raft and purlins	5	01-Jun-26	06-Jun-26	25-Jun-26 A	25-Jun-26 A	326,261.32	326,261.32	326,261.32	100%	100%
DAM3-C-B4-A-1430	Intumescent paint to steel works	7	07-Jun-26	14-Jun-26	08-Jul-26 A	14-Jul-26 A	317,759.56	317,759.56	317,759.56	100%	100%
DAM3-C-B4-A-250	Installation of roof sheet	5	21-Jun-26	25-Jun-26	26-Jul-26 A	30-Jul-26 A	217,507.55	217,507.55	217,507.55	100%	100%
DAM3-C-B4-SS-1030	Steel members for external platform	7	23-Jun-26	30-Jun-26	01-Sep-26 A	02-Sep-26 A	18,670.78	18,670.78	18,670.78	100%	100%
DAM3-C-B4-A-1440	Steel members for office area	7	15-Jun-26	22-Jun-26	01-Oct-26 A	04-Oct-26 A	115,805.20	115,805.20	115,805.20	100%	100%
DAM3-C-B4-A-240	Installation of wall sandwich panel	5	14-Jul-26	19-Jul-26	03-Oct-26 A	28-Oct-26 A	326,261.32	326,261.32	326,261.32	100%	100%
DAM3-C-B4-SS-1040	Epoxy paint for external platform	5	01-Jul-26	06-Jul-26	06-Oct-26	11-Oct-26	3,734.16	3,734.16	0.00	100%	0%
DAM3-C-B4-SS-1020	Epoxy paint to steel members at office area	7	28-Jun-26	05-Jul-26	14-Oct-26	21-Oct-26	23,161.04	23,161.04	0.00	100%	0%
ARCHITECTURAL		112	09-Jun-26	17-Oct-26	03-Aug-26 A	26-Dec-26	900,244.66	765,935.70	133,999.53	85.08%	14.88%
MASONARY WORKS		30	09-Jun-26	21-Jul-26	05-Aug-26 A	01-Sep-26 A	78,954.21	78,954.21	78,954.21	100%	100%
DAM3-C-B4-A-1030	Block work at toilet area	7	14-Jul-26	21-Jul-26	05-Aug-26 A	24-Aug-26 A	14,436.31	14,436.31	14,436.31	100%	100%
DAM3-C-B4-A-230	Block work at factory area	10	09-Jun-26	20-Jun-26	05-Aug-26 A	10-Aug-26 A	58,338.72	58,338.72	58,338.72	100%	100%
DAM3-C-B4-A-260	Block work at office area	7	06-Jul-26	13-Jul-26	05-Aug-26 A	01-Sep-26 A	6,179.18	6,179.18	6,179.18	100%	100%
WALL FINISHES		25	01-Aug-26	15-Sep-26	24-Sep-26 A	28-Nov-26	92,757.47	92,757.47	48,590.16	100%	52.38%
DAM3-C-B4-A-1040	Internal Wall Plaster	10	01-Aug-26	17-Aug-26	24-Sep-26 A	06-Oct-26 A	48,590.16	48,590.16	48,590.16	100%	100%
DAM3-C-B4-A-1090	Paint to Plaster (Primer, Putty & First Coat)	7	08-Sep-26	15-Sep-26	21-Nov-26	28-Nov-26	44,167.30	44,167.30	0.00	100%	0%
CIELING FINISHES		5	31-Aug-26	05-Sep-26	12-Nov-26	17-Nov-26	46,792.30	46,792.30	0.00	100%	0%
DAM3-C-B4-A-1100	Installation of Ceiling Gypsum Board	5	31-Aug-26	05-Sep-26	12-Nov-26	17-Nov-26	46,792.30	46,792.30	0.00	100%	0%
FLOOR FINISHES		45	23-Aug-26	17-Oct-26	04-Nov-26	26-Dec-26	189,488.90	74,069.14	0.00	39.09%	0%
DAM3-C-B4-A-1080	Tiles for Toilet	7	23-Aug-26	30-Aug-26	04-Nov-26	11-Nov-26	46,530.71	46,530.71	0.00	100%	0%
DAM3-C-B4-A-1110	Tiles for Office Area	2	06-Sep-26	07-Sep-26	18-Nov-26	19-Nov-26	26,867.31	26,867.31	0.00	100%	0%
DAM3-C-B4-A-1240	Granite strip	2	08-Sep-26	09-Sep-26	21-Nov-26	22-Nov-26	671.12	671.12	0.00	100%	0%
DAM3-C-B4-A-1260	Epoxy paint	7	10-Oct-26	17-Oct-26	19-Dec-26	26-Dec-26	115,419.76	0.00	0.00	0%	0%
DOORS & WINDOWS		14	20-Jul-26	04-Aug-26	22-Oct-26	07-Nov-26	248,575.06	248,575.06	0.00	100%	0%
DAM3-C-B4-A-1420	Window (CW1)	7	20-Jul-26	27-Jul-26	22-Oct-26	29-Oct-26	94,173.21	94,173.21	0.00	100%	0%
DAM3-C-B4-A-1050	Roll up Shutter Door	1	28-Jul-26	28-Jul-26	31-Oct-26	31-Oct-26	68,619.20	68,619.20	0.00	100%	0%
DAM3-C-B4-A-1060	Supply and install (D5) 1000*2200mm single leaf steel door with door	1	29-Jul-26	29-Jul-26	01-Nov-26	01-Nov-26	16,016.16	16,016.16	0.00	100%	0%
DAM3-C-B4-A-1120	Supply and install (D4) 800*2200 mm single leaf aluminum door with door	1	30-Jul-26	30-Jul-26	02-Nov-26	02-Nov-26	22,737.85	22,737.85	0.00	100%	0%
DAM3-C-B4-A-1130	Supply and install (D7) 1000*2200 mm single leaf aluminum door with door	1	01-Aug-26	01-Aug-26	03-Nov-26	03-Nov-26	7,811.07	7,811.07	0.00	100%	0%
DAM3-C-B4-A-1350	Supply and install (D3) 1000*2200 mm single leaf aluminum door with door	1	02-Aug-26	02-Aug-26	04-Nov-26	04-Nov-26	16,016.16	16,016.16	0.00	100%	0%
DAM3-C-B4-A-1360	Supply and install fire rated 45 min (D2) 1200*2200 mm single leaf steel doo	1	03-Aug-26	03-Aug-26	05-Nov-26	05-Nov-26	16,711.52	16,711.52	0.00	100%	0%
DAM3-C-B4-A-1370	Skylight fixtures installation	1	04-Aug-26	04-Aug-26	07-Nov-26	07-Nov-26	6,489.89	6,489.89	0.00	100%	0%
WATER PROOFING WORKS		4	18-Aug-26	22-Aug-26	31-Oct-26	03-Nov-26	4,879.02	4,879.02	0.00	100%	0%
DAM3-C-B4-A-1220	Waterproofing membrane for toilets	4	18-Aug-26	22-Aug-26	31-Oct-26	03-Nov-26	4,879.02	4,879.02	0.00	100%	0%
METAL WORKS		19	10-Sep-26	26-Sep-26	03-Aug-26 A	05-Dec-26	193,717.06	193,717.06	6,455.16	100%	3.33%
DAM3-C-B4-A-1160	Galvanised Steel Gratings	2	24-Sep-26	26-Sep-26	03-Aug-26 A	03-Aug-26 A	6,455.16	6,455.16	6,455.16	100%	100%
DAM3-C-B4-A-1150	Steel Ladder	2	10-Sep-26	12-Sep-26	23-Nov-26	24-Nov-26	9,839.16	9,839.16	0.00	100%	0%
DAM3-C-B4-A-1250	Steel railing works	4	13-Sep-26	16-Sep-26	25-Nov-26	29-Nov-26	1,533.98	1,533.98	0.00	100%	0%
DAM3-C-B4-A-1170	Aluminium composite panel	5	17-Sep-26	22-Sep-26	30-Nov-26	05-Dec-26	175,888.76	175,888.76	0.00	100%	0%
SPECIALTIES		11	27-Sep-26	08-Oct-26	06-Dec-26	17-Dec-26	45,080.66	26,191.45	0.00	58.1%	0%
DAM3-C-B4-A-1180	Installation of fittings	7	27-Sep-26	04-Oct-26	06-Dec-26	13-Dec-26	22,981.27	22,981.27	0.00	100%	0%
DAM3-C-B4-A-1410	Identification sign; ID01 & ID02	3	05-Oct-26	07-Oct-26	14-Dec-26	16-Dec-26	9,630.56	3,210.19	0.00	33.33%	0%
DAM3-C-B4-A-1200	Furniture Installation	1	08-Oct-26	08-Oct-26	17-Dec-26	17-Dec-26	12,468.83	0.00	0.00	0%	0%
MECHANICAL		150	07-May-26	06-Oct-26	25-Jun-26 A	17-Dec-26	467,522.66	466,620.64	156,280.78	99.81%	33.43%
HVAC		14	16-Sep-26	03-Oct-26	29-Nov-26	14-Dec-26	233,183.33	233,183.33	0.00	100%	0%

Activity ID	Activity Name	Original Duration	BL Project Start	BL Project Finish	Start	Finish	Budgeted Total Cost	Planned Value Cost	Earned Value Cost	Schedule % Complete	Performance % Complete
FIRST STAGE		4	24-Sep-26	28-Sep-26	06-Dec-26	09-Dec-26	170,694.73	170,694.73	0.00	100%	0%
DAM3-C-B4-M-760	Installation of HVAC Ducts	2	24-Sep-26	26-Sep-26	06-Dec-26	07-Dec-26	149,489.33	149,489.33	0.00	100%	0%
DAM3-C-B4-M-790	Installation of Duct insulation	2	27-Sep-26	28-Sep-26	08-Dec-26	09-Dec-26	21,205.40	21,205.40	0.00	100%	0%
SECOND STAGE		14	16-Sep-26	03-Oct-26	29-Nov-26	14-Dec-26	62,488.60	62,488.60	0.00	100%	0%
DAM3-C-B4-M-750	Installation of Exhaust Fans	2	16-Sep-26	17-Sep-26	29-Nov-26	30-Nov-26	7,938.56	7,938.56	0.00	100%	0%
DAM3-C-B4-M-780	Installation of Wall Propeller Type Exhaust Fan	4	19-Sep-26	22-Sep-26	01-Dec-26	05-Dec-26	46,831.64	46,831.64	0.00	100%	0%
DAM3-C-B4-M-770	Installation of Diffuser	2	29-Sep-26	30-Sep-26	10-Dec-26	12-Dec-26	2,144.00	2,144.00	0.00	100%	0%
DAM3-C-B4-M-960	Supply, install, test and commission door grilles & exhaust louvers	2	01-Oct-26	03-Oct-26	13-Dec-26	14-Dec-26	5,574.40	5,574.40	0.00	100%	0%
FIRE FIGHTING SYSTEM		20	16-Sep-26	06-Oct-26	30-Sep-26 A	17-Dec-26	102,458.78	101,556.76	84,594.16	99.12%	82.56%
FIRST STAGE		12	16-Sep-26	30-Sep-26	30-Sep-26 A	04-Oct-26 A	84,594.16	84,594.16	84,594.16	100%	100%
DAM3-C-B4-M-920	Installation of Fire Fighting Pipes (Seamless Black Steel)	7	16-Sep-26	24-Sep-26	30-Sep-26 A	04-Oct-26 A	72,394.75	72,394.75	72,394.75	100%	100%
DAM3-C-B4-M-930	Installation of Fire Fighting Valve	5	26-Sep-26	30-Sep-26	30-Sep-26 A	04-Oct-26 A	12,199.40	12,199.40	12,199.40	100%	100%
SECOND STAGE		17	01-Oct-26	06-Oct-26	29-Nov-26	17-Dec-26	17,864.62	16,962.60	0.00	94.95%	0%
DAM3-C-B4-M-940	Installation of Fire Hose Cabinet	3	01-Oct-26	04-Oct-26	29-Nov-26	01-Dec-26	15,158.56	15,158.56	0.00	100%	0%
DAM3-C-B4-M-990	Supply, install, test and commission Fire Department Connection(FDC)	3	04-Oct-26	06-Oct-26	15-Dec-26	17-Dec-26	2,706.06	1,804.04	0.00	66.67%	0%
SEWER AND DRAINAGE SYSTEM		132	07-May-26	24-Sep-26	25-Jun-26 A	30-Nov-26	90,009.74	90,009.74	30,093.94	100%	33.43%
FIRST STAGE		118	07-May-26	07-Sep-26	25-Jun-26 A	14-Nov-26	41,149.90	41,149.90	30,093.94	100%	73.13%
DAM3-C-B4-M-1000	Installation of Trench drain	5	02-Sep-26	07-Sep-26	25-Jun-26 A	28-Jun-26 A	11,508.80	11,508.80	11,508.80	100%	100%
DAM3-C-B4-M-820	Installation of Sanitary Waste / Drainage Pipes	4	07-May-26	11-May-26	27-Jun-26 A	29-Jun-26 A	18,585.14	18,585.14	18,585.14	100%	100%
DAM3-C-B4-M-840	Installation of Floor Drain	2	31-Aug-26	01-Sep-26	12-Nov-26	14-Nov-26	11,055.96	11,055.96	0.00	100%	0%
SECOND STAGE		14	08-Sep-26	24-Sep-26	15-Nov-26	30-Nov-26	48,859.84	48,859.84	0.00	100%	0%
DAM3-C-B4-M-800	Installation of Electric Water Heater	2	08-Sep-26	09-Sep-26	15-Nov-26	16-Nov-26	1,819.51	1,819.51	0.00	100%	0%
DAM3-C-B4-M-810	Installation of Sanitary Fixture and Accessories	4	10-Sep-26	14-Sep-26	17-Nov-26	21-Nov-26	19,921.72	19,921.72	0.00	100%	0%
DAM3-C-B4-M-830	Installation of Lavotary /Wash Basin	2	15-Sep-26	16-Sep-26	22-Nov-26	23-Nov-26	21,416.68	21,416.68	0.00	100%	0%
DAM3-C-B4-M-890	Installation of Bib Tap	2	17-Sep-26	19-Sep-26	24-Nov-26	25-Nov-26	1,900.66	1,900.66	0.00	100%	0%
DAM3-C-B4-M-850	Installation of Water Tap	2	20-Sep-26	21-Sep-26	26-Nov-26	28-Nov-26	2,874.14	2,874.14	0.00	100%	0%
DAM3-C-B4-M-860	Installation of Roof Vent Cap	2	22-Sep-26	24-Sep-26	29-Nov-26	30-Nov-26	927.12	927.12	0.00	100%	0%
WATER SUPPLY SYSTEM		13	16-Sep-26	29-Sep-26	22-Sep-26 A	03-Dec-26	41,870.81	41,870.81	41,592.68	100%	99.34%
FIRST STAGE		7	16-Sep-26	22-Sep-26	22-Sep-26 A	29-Sep-26 A	41,592.68	41,592.68	41,592.68	100%	100%
DAM3-C-B4-M-910	Installation of Water Supply Pipes	4	16-Sep-26	20-Sep-26	22-Sep-26 A	29-Sep-26 A	23,318.41	23,318.41	23,318.41	100%	100%
DAM3-C-B4-M-900	Installation of Water Supply Valve	2	21-Sep-26	22-Sep-26	24-Sep-26 A	29-Sep-26 A	18,274.27	18,274.27	18,274.27	100%	100%
SECOND STAGE		5	24-Sep-26	29-Sep-26	29-Nov-26	03-Dec-26	278.13	278.13	0.00	100%	0%
DAM3-C-B4-M-950	Capped connection	5	24-Sep-26	29-Sep-26	29-Nov-26	03-Dec-26	278.13	278.13	0.00	100%	0%
ELECTRICAL		101	22-Jul-26	01-Dec-26	24-May-26 A	04-Jan-27	752,044.76	102,181.36	27,642.87	13.59%	3.68%
FIRST STAGE		100	22-Jul-26	28-Oct-26	24-May-26 A	03-Jan-27	86,114.12	4,688.76	27,642.87	5.44%	32.1%
DAM3-C-B4-E-573	Installation of Earthing and Grounding	4	25-Oct-26	28-Oct-26	24-May-26 A	30-Dec-26	19,646.47	0.00	17,681.82	0%	90%
DAM3-C-B4-E-603	Installation of Conduits and wiring outlets - Fire Alarm System	4	24-Sep-26	28-Sep-26	24-May-26 A	07-Dec-26	1,768.31	1,768.31	884.15	100%	50%
DAM3-C-B4-E-643	Installation of Sleeves & Power outlet	8	22-Jul-26	30-Jul-26	24-May-26 A	26-Oct-26	2,920.45	2,920.45	1,460.23	100%	50%
DAM3-C-B4-E-623	Installation of Conduites for Lighting Fixture	4	08-Oct-26	12-Oct-26	12-Sep-26 A	17-Dec-26	8,462.97	0.00	7,616.67	0%	90%
DAM3-C-B4-E-693	Installation of Wires	4	13-Oct-26	17-Oct-26	19-Dec-26	22-Dec-26	16,925.94	0.00	0.00	0%	0%
DAM3-C-B4-E-683	Installation of LV Cables	4	25-Oct-26	28-Oct-26	30-Dec-26	03-Jan-27	36,389.98	0.00	0.00	0%	0%
SECOND STAGE		57	16-Sep-26	01-Dec-26	31-Oct-26	04-Jan-27	665,930.64	97,492.60	0.00	14.64%	0%
DAM3-C-B4-E-1040	Installation of Solar power plant	7	24-Nov-26	01-Dec-26	31-Oct-26	07-Nov-26	253,268.71	0.00	0.00	0%	0%
DAM3-C-B4-E-633	Installation of Wiring Devices	4	16-Sep-26	20-Sep-26	29-Nov-26	02-Dec-26	19,435.09	19,435.09	0.00	100%	0%
DAM3-C-B4-E-663	Installation of Disconnect Switches	2	21-Sep-26	22-Sep-26	03-Dec-26	05-Dec-26	30,235.95	30,235.95	0.00	100%	0%
DAM3-C-B4-E-583	Installation of Fire Alarm Control Panel	4	29-Sep-26	03-Oct-26	08-Dec-26	12-Dec-26	19,451.37	19,451.37	0.00	100%	0%
DAM3-C-B4-E-593	Installation of Fire Detectors & Accessories	4	04-Oct-26	07-Oct-26	13-Dec-26	16-Dec-26	56,740.37	28,370.18	0.00	50%	0%
DAM3-C-B4-E-733	Installation of Access Control System	5	08-Oct-26	13-Oct-26	17-Dec-26	22-Dec-26	27,616.86	0.00	0.00	0%	0%
DAM3-C-B4-E-613	Installation of Lighting fixtures	4	18-Oct-26	21-Oct-26	23-Dec-26	27-Dec-26	76,166.74	0.00	0.00	0%	0%

Date	Revision	Checked	Approved
06-Oct-26	Weekly Report		

Activity ID	Activity Name	Original Duration	BL Project Start	BL Project Finish	Start	Finish	Budgeted Total Cost	Planned Value Cost	Earned Value Cost	Schedule % Complete	Performance % Complete
DAM3-C-B4-E-653	Installation of Main Distribution Board	2	18-Oct-26	19-Oct-26	23-Dec-26	24-Dec-26	32,472.73	0.00	0.00	0%	0%
DAM3-C-B4-E-743	Monitor Modules for Fire Alarm	2	14-Oct-26	15-Oct-26	23-Dec-26	24-Dec-26	3,882.38	0.00	0.00	0%	0%
DAM3-C-B4-E-703	Installation of LP-1 Panel	2	20-Oct-26	21-Oct-26	26-Dec-26	27-Dec-26	18,403.54	0.00	0.00	0%	0%
DAM3-C-B4-E-753	Line Isolator Modules for Fire Alarm	2	17-Oct-26	18-Oct-26	26-Dec-26	27-Dec-26	185.40	0.00	0.00	0%	0%
DAM3-C-B4-E-1030	Installation of CCTV System	7	22-Oct-26	29-Oct-26	28-Dec-26	04-Jan-27	76,349.24	0.00	0.00	0%	0%
DAM3-C-B4-E-713	Installation of PP-AC panel	2	22-Oct-26	24-Oct-26	28-Dec-26	29-Dec-26	21,648.48	0.00	0.00	0%	0%
DAM3-C-B4-E-763	Firewarning flash light with sounder; wall mounted, Weather proof	2	19-Oct-26	20-Oct-26	28-Dec-26	29-Dec-26	3,082.69	0.00	0.00	0%	0%
DAM3-C-B4-E-673	Installation of Telephone Cabinet	2	25-Oct-26	26-Oct-26	30-Dec-26	31-Dec-26	26,991.08	0.00	0.00	0%	0%
BLOCK B3		303	03-Mar-26	28-Dec-26	17-Feb-26 A	20-Feb-27	5,075,523.09	3,476,170.36	2,720,525.80	68.49%	53.6%
STRUCTURAL		175	03-Mar-26	18-Jul-26	17-Feb-26 A	21-Oct-26	1,389,042.53	1,389,042.53	1,379,773.47	100%	99.33%
FOOTING		46	03-Mar-26	04-Apr-26	17-Feb-26 A	17-May-26 A	597,655.16	597,655.16	597,655.16	100%	100%
DAM3-C-B3-S-210	Excavation for footings	4	03-Mar-26	07-Mar-26	17-Feb-26 A	12-Mar-26 A	89,859.61	89,859.61	89,859.61	100%	100%
DAM3-C-B3-S-6203	Soil replacement - rock fill	4	08-Mar-26	11-Mar-26	17-Mar-26 A	24-Mar-26 A	179,061.91	179,061.91	179,061.91	100%	100%
DAM3-C-B3-S-6213	Engineering fill	4	12-Mar-26	16-Mar-26	28-Mar-26 A	07-Apr-26 A	46,046.19	46,046.19	46,046.19	100%	100%
DAM3-C-B3-S-797	Lean Concrete Below Footings	2	23-Mar-26	24-Mar-26	11-Apr-26 A	11-Apr-26 A	8,229.34	8,229.34	8,229.34	100%	100%
DAM3-C-B3-S-947	Vapour Barrier for Footings	1	22-Mar-26	22-Mar-26	11-Apr-26 A	11-Apr-26 A	7,940.10	7,940.10	7,940.10	100%	100%
DAM3-C-B3-S-1037	Anti Termite Below Footings	1	21-Mar-26	21-Mar-26	11-Apr-26 A	11-Apr-26 A	11,905.55	11,905.55	11,905.55	100%	100%
DAM3-C-B3-S-847	Rebar for Footings	4	25-Mar-26	29-Mar-26	06-May-26 A	11-May-26 A	101,844.98	101,844.98	101,844.98	100%	100%
DAM3-C-B3-S-857	Formwork for Footings	4	30-Mar-26	02-Apr-26	11-May-26 A	13-May-26 A	25,461.25	25,461.25	25,461.25	100%	100%
DAM3-C-B3-S-807	Pouring Concrete for Footings	1	04-Apr-26	04-Apr-26	17-May-26 A	17-May-26 A	127,306.23	127,306.23	127,306.23	100%	100%
COLUMN NECK		12	05-Apr-26	20-Apr-26	11-May-26 A	09-Jun-26 A	120,554.54	120,554.54	120,554.54	100%	100%
DAM3-C-B3-S-897	Rebar for column neck	2	05-Apr-26	06-Apr-26	11-May-26 A	14-May-26 A	14,919.19	14,919.19	14,919.19	100%	100%
DAM3-C-B3-S-887	Pouring Concrete for column neck	1	09-Apr-26	09-Apr-26	20-May-26 A	20-May-26 A	24,865.31	24,865.31	24,865.31	100%	100%
DAM3-C-B3-S-937	Damp proof /Bitumin paint on Footings & column neck	2	11-Apr-26	12-Apr-26	20-May-26 A	23-May-26 A	24,777.73	24,777.73	24,777.73	100%	100%
DAM3-C-B3-S-907	Formwork for column neck	2	07-Apr-26	08-Apr-26	21-May-26 A	23-May-26 A	9,946.13	9,946.13	9,946.13	100%	100%
DAM3-C-B3-S-997	Backfilling / Compaction up to Bottom of Grade Beams	7	13-Apr-26	20-Apr-26	24-May-26 A	09-Jun-26 A	46,046.19	46,046.19	46,046.19	100%	100%
GRADE BEAM		15	21-Apr-26	11-May-26	14-Jun-26 A	30-Jun-26 A	171,632.86	171,632.86	171,632.86	100%	100%
DAM3-C-B3-S-817	Lean Concrete Below Grade Beams	2	25-Apr-26	26-Apr-26	14-Jun-26 A	14-Jun-26 A	4,431.19	4,431.19	4,431.19	100%	100%
DAM3-C-B3-S-967	Vapour barrier for Grade Beams	2	22-Apr-26	23-Apr-26	14-Jun-26 A	14-Jun-26 A	5,293.40	5,293.40	5,293.40	100%	100%
DAM3-C-B3-S-1047	Anti Termite Below Grade Beams	1	21-Apr-26	21-Apr-26	14-Jun-26 A	14-Jun-26 A	11,905.55	11,905.55	11,905.55	100%	100%
DAM3-C-B3-S-867	Rebar for Grade Beams	5	27-Apr-26	02-May-26	16-Jun-26 A	20-Jun-26 A	27,194.46	27,194.46	27,194.46	100%	100%
DAM3-C-B3-S-877	Formwork for Grade Beams	2	03-May-26	04-May-26	18-Jun-26 A	22-Jun-26 A	6,798.61	6,798.61	6,798.61	100%	100%
DAM3-C-B3-S-1027	Anchor bolts installation	2	03-May-26	04-May-26	18-Jun-26 A	20-Jun-26 A	57,238.83	57,238.83	57,238.83	100%	100%
DAM3-C-B3-S-827	Pouring Concrete for Grade Beams	1	05-May-26	05-May-26	24-Jun-26 A	24-Jun-26 A	33,993.09	33,993.09	33,993.09	100%	100%
DAM3-C-B3-S-977	Damp proof /Bitumin paint on Grade Beams	5	06-May-26	11-May-26	27-Jun-26 A	30-Jun-26 A	24,777.73	24,777.73	24,777.73	100%	100%
SLAB ON GRADE		92	12-May-26	18-Jul-26	06-Jul-26 A	21-Oct-26	397,232.98	397,232.98	396,325.87	100%	99.77%
DAM3-C-B3-S-1007	Backfilling / Compaction for Slab on Grade	7	12-May-26	19-May-26	06-Jul-26 A	09-Jul-26 A	23,023.09	23,023.09	23,023.09	100%	100%
DAM3-C-B3-S-837	Pouring Concrete for Ground Slab	4	24-May-26	31-May-26	11-Aug-26 A	15-Aug-26 A	344,195.21	344,195.21	344,195.21	100%	100%
DAM3-C-B3-S-957	Anti Termite Treatment below Ground Slab	1	20-May-26	20-May-26	11-Aug-26 A	15-Aug-26 A	15,874.08	15,874.08	15,874.08	100%	100%
DAM3-C-B3-S-987	Vapour barrier for below Ground Slab	2	21-May-26	23-May-26	11-Aug-26 A	15-Aug-26 A	13,233.49	13,233.49	13,233.49	100%	100%
DAM3-C-B3-S-1017	Concrete pad	7	11-Jul-26	18-Jul-26	14-Oct-26	21-Oct-26	907.11	907.11	0.00	100%	0%
COLUMNS & BEAMS		59	20-May-26	20-Jun-26	16-Jun-26 A	06-Oct-26	101,966.98	101,966.98	93,605.04	100%	91.8%
DAM3-C-B3-S-6101	Rebar for Tie Beams	4	04-Jun-26	08-Jun-26	16-Jun-26 A	20-Jun-26 A	7,263.64	7,263.64	7,263.64	100%	100%
DAM3-C-B3-S-6102	Formwork for Tie Beams	2	09-Jun-26	10-Jun-26	18-Jun-26 A	22-Jun-26 A	1,815.91	1,815.91	1,815.91	100%	100%
DAM3-C-B3-S-6103	Pouring Concrete for Tie Beams	1	11-Jun-26	11-Jun-26	24-Jun-26 A	24-Jun-26 A	9,079.54	9,079.54	9,079.54	100%	100%
DAM3-C-B3-S-5101	Rebar for column	5	20-May-26	25-May-26	22-Jul-26 A	25-Jul-26 A	20,144.05	20,144.05	20,144.05	100%	100%
DAM3-C-B3-S-5102	Formwork for column	4	30-May-26	02-Jun-26	27-Jul-26 A	02-Aug-26 A	5,036.01	5,036.01	5,036.01	100%	100%
DAM3-C-B3-S-5103	Pouring Concrete for column	1	03-Jun-26	03-Jun-26	29-Jul-26 A	03-Aug-26 A	25,180.06	25,180.06	25,180.06	100%	100%
DAM3-C-B3-S-6113	Rebar for Beams	4	13-Jun-26	16-Jun-26	08-Sep-26 A	15-Sep-26 A	13,379.11	13,379.11	13,379.11	100%	100%


Activity ID	Activity Name	Original Duration	BL Project Start	BL Project Finish	Start	Finish	Budgeted Total Cost	Planned Value Cost	Earned Value Cost	Schedule % Complete	Performance % Complete
DAM3-C-B3-S-6123	Formwork for Beams	2	17-Jun-26	18-Jun-26	23-Sep-26 A	29-Sep-26 A	3,344.77	3,344.77	3,344.77	100%	100%
DAM3-C-B3-S-6133	Pouring Concrete for Beams	1	20-Jun-26	20-Jun-26	26-Sep-26 A	06-Oct-26	16,723.88	16,723.88	8,361.94	100%	50%
STRUCTURAL STEEL		81	07-Jun-26	15-Jul-26	15-Jul-26 A	27-Oct-26	1,566,668.48	1,566,668.48	1,079,035.98	100%	68.87%
DAM3-C-B3-A-210	Installation of columns	3	07-Jun-26	09-Jun-26	15-Jul-26 A	15-Jul-26 A	217,507.55	217,507.55	217,507.55	100%	100%
DAM3-C-B3-A-220	Installation of raft and purlins	5	10-Jun-26	15-Jun-26	15-Jul-26 A	16-Jul-26 A	326,261.32	326,261.32	326,261.32	100%	100%
DAM3-C-B3-A-1430	Intumescent paint to steel works	7	16-Jun-26	23-Jun-26	25-Jul-26 A	29-Jul-26 A	317,759.56	317,759.56	317,759.56	100%	100%
DAM3-C-B3-A-250	Installation of roof sheet	5	02-Jul-26	07-Jul-26	16-Aug-26 A	23-Aug-26 A	217,507.55	217,507.55	217,507.55	100%	100%
DAM3-C-B3-A-1440	Steel members for office area	7	24-Jun-26	01-Jul-26	06-Oct-26	13-Oct-26	115,805.20	115,805.20	0.00	100%	0%
DAM3-C-B3-A-240	Installation of wall sandwich panel	5	11-Jul-26	15-Jul-26	14-Oct-26	19-Oct-26	326,261.32	326,261.32	0.00	100%	0%
DAM3-C-B3-SS-1020	Epoxy paint to steel members at office area	7	02-Jul-26	09-Jul-26	14-Oct-26	21-Oct-26	23,161.04	23,161.04	0.00	100%	0%
DAM3-C-B3-SS-1030	Steel members for external platform	7	02-Jul-26	09-Jul-26	14-Oct-26	21-Oct-26	18,670.78	18,670.78	0.00	100%	0%
DAM3-C-B3-SS-1040	Epoxy paint for external platform	5	11-Jul-26	15-Jul-26	22-Oct-26	27-Oct-26	3,734.16	3,734.16	0.00	100%	0%
ARCHITECTURAL		146	21-Jun-26	20-Dec-26	18-Aug-26 A	11-Feb-27	900,244.66	427,529.16	85,409.37	47.49%	9.49%
MASONARY WORKS		25	21-Jun-26	18-Jul-26	24-Aug-26 A	09-Sep-26 A	78,954.21	78,954.21	78,954.21	100%	100%
DAM3-C-B3-A-230	Block work at factory area	10	21-Jun-26	01-Jul-26	24-Aug-26 A	01-Sep-26 A	58,338.72	58,338.72	58,338.72	100%	100%
DAM3-C-B3-A-1030	Block work at toilet area	7	11-Jul-26	18-Jul-26	25-Aug-26 A	03-Sep-26 A	14,436.31	14,436.31	14,436.31	100%	100%
DAM3-C-B3-A-260	Block work at office area	7	02-Jul-26	09-Jul-26	25-Aug-26 A	09-Sep-26 A	6,179.18	6,179.18	6,179.18	100%	100%
WALL FINISHES		74	28-Jul-26	19-Nov-26	25-Oct-26	18-Jan-27	92,757.47	48,590.16	0.00	52.38%	0%
DAM3-C-B3-A-1040	Internal Wall Plaster	10	28-Jul-26	13-Aug-26	25-Oct-26	05-Nov-26	48,590.16	48,590.16	0.00	100%	0%
DAM3-C-B3-A-1090	Paint to Plaster (Primer, Putty & First Coat)	2	12-Nov-26	19-Nov-26	17-Jan-27	18-Jan-27	44,167.30	0.00	0.00	0%	0%
CIELING FINISHES		5	04-Nov-26	09-Nov-26	09-Jan-27	13-Jan-27	46,792.30	0.00	0.00	0%	0%
DAM3-C-B3-A-1100	Installation of Ceiling Gypsum Board	5	04-Nov-26	09-Nov-26	09-Jan-27	13-Jan-27	46,792.30	0.00	0.00	0%	0%
FLOOR FINISHES		81	19-Aug-26	20-Dec-26	10-Nov-26	11-Feb-27	189,488.90	46,530.71	0.00	24.56%	0%
DAM3-C-B3-A-1080	Tiles for Toilet	7	19-Aug-26	26-Aug-26	10-Nov-26	18-Nov-26	46,530.71	46,530.71	0.00	100%	0%
DAM3-C-B3-A-1110	Tiles for Office Area	2	10-Nov-26	11-Nov-26	14-Jan-27	16-Jan-27	26,867.31	0.00	0.00	0%	0%
DAM3-C-B3-A-1240	Granite strip	2	12-Nov-26	14-Nov-26	17-Jan-27	18-Jan-27	671.12	0.00	0.00	0%	0%
DAM3-C-B3-A-1260	Epoxy paint	3	13-Dec-26	20-Dec-26	09-Feb-27	11-Feb-27	115,419.76	0.00	0.00	0%	0%
DOORS & WINDOWS		14	16-Jul-26	01-Aug-26	20-Oct-26	04-Nov-26	248,575.06	248,575.06	0.00	100%	0%
DAM3-C-B3-A-1420	Window (CW1)	7	16-Jul-26	23-Jul-26	20-Oct-26	27-Oct-26	94,173.21	94,173.21	0.00	100%	0%
DAM3-C-B3-A-1050	Roll up Shutter Door	1	25-Jul-26	25-Jul-26	28-Oct-26	28-Oct-26	68,619.20	68,619.20	0.00	100%	0%
DAM3-C-B3-A-1060	Supply and install (D5) 1000*2200mm single leaf steel door with door	1	26-Jul-26	26-Jul-26	29-Oct-26	29-Oct-26	16,016.16	16,016.16	0.00	100%	0%
DAM3-C-B3-A-1120	Supply and install (D4) 800*2200 mm single leaf aluminum door with door	1	27-Jul-26	27-Jul-26	31-Oct-26	31-Oct-26	22,737.85	22,737.85	0.00	100%	0%
DAM3-C-B3-A-1130	Supply and install (D7) 1000*2200 mm single leaf aluminum door with door	1	28-Jul-26	28-Jul-26	01-Nov-26	01-Nov-26	7,811.07	7,811.07	0.00	100%	0%
DAM3-C-B3-A-1350	Supply and install (D3) 1000*2200 mm single leaf aluminum door with door	1	29-Jul-26	29-Jul-26	02-Nov-26	02-Nov-26	16,016.16	16,016.16	0.00	100%	0%
DAM3-C-B3-A-1360	Supply and install fire rated 45 min (D2) 1200*2200 mm single leaf steel doo	1	30-Jul-26	30-Jul-26	03-Nov-26	03-Nov-26	16,711.52	16,711.52	0.00	100%	0%
DAM3-C-B3-A-1370	Skylight fixtures installation	1	01-Aug-26	01-Aug-26	04-Nov-26	04-Nov-26	6,489.89	6,489.89	0.00	100%	0%
WATER PROOFING WORKS		4	15-Aug-26	18-Aug-26	05-Nov-26	10-Nov-26	4,879.02	4,879.02	0.00	100%	0%
DAM3-C-B3-A-1220	Waterproofing membrane for toilets	4	15-Aug-26	18-Aug-26	05-Nov-26	10-Nov-26	4,879.02	4,879.02	0.00	100%	0%
METAL WORKS		22	15-Nov-26	29-Nov-26	18-Aug-26 A	31-Jan-27	193,717.06	0.00	6,455.16	0%	3.33%
DAM3-C-B3-A-1160	Galvanised Steel Gratings	2	28-Nov-26	29-Nov-26	18-Aug-26 A	18-Aug-26 A	6,455.16	0.00	6,455.16	0%	100%
DAM3-C-B3-A-1150	Steel Ladder	2	15-Nov-26	16-Nov-26	19-Jan-27	20-Jan-27	9,839.16	0.00	0.00	0%	0%
DAM3-C-B3-A-1250	Steel railing works	4	17-Nov-26	21-Nov-26	21-Jan-27	25-Jan-27	1,533.98	0.00	0.00	0%	0%
DAM3-C-B3-A-1170	Aluminium composite panel	5	22-Nov-26	26-Nov-26	26-Jan-27	31-Jan-27	175,888.76	0.00	0.00	0%	0%
SPECIALTIES		7	30-Nov-26	12-Dec-26	01-Feb-27	08-Feb-27	45,080.66	0.00	0.00	0%	0%
DAM3-C-B3-A-1180	Installation of fittings	3	30-Nov-26	07-Dec-26	01-Feb-27	03-Feb-27	22,981.27	0.00	0.00	0%	0%
DAM3-C-B3-A-1410	Identification sign; ID01 & ID02	3	08-Dec-26	10-Dec-26	04-Feb-27	07-Feb-27	9,630.56	0.00	0.00	0%	0%
DAM3-C-B3-A-1200	Furniture Installation	1	12-Dec-26	12-Dec-26	08-Feb-27	08-Feb-27	12,468.83	0.00	0.00	0%	0%
MECHANICAL		163	12-May-26	09-Dec-26	30-Jul-26 A	07-Feb-27	467,522.66	90,009.74	156,280.78	19.25%	33.43%
HVAC		14	21-Nov-26	06-Dec-26	19-Jan-27	03-Feb-27	233,183.33	0.00	0.00	0%	0%

2026 2027

Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary

Date	Revision	Checked	Approved
06-Oct-26	Weekly Report		

Activity ID	Activity Name	Original Duration	BL Project Start	BL Project Finish	Start	Finish	Budgeted Total Cost	Planned Value Cost	Earned Value Cost	Schedule % Complete	Performance % Complete
FIRST STAGE		4	28-Nov-26	01-Dec-26	26-Jan-27	30-Jan-27	170,694.73	0.00	0.00	0%	0%
DAM3-C-B3-M-760	Installation of HVAC Ducts	2	28-Nov-26	29-Nov-26	26-Jan-27	27-Jan-27	149,489.33	0.00	0.00	0%	0%
DAM3-C-B3-M-790	Installation of Duct insulation	2	30-Nov-26	01-Dec-26	28-Jan-27	30-Jan-27	21,205.40	0.00	0.00	0%	0%
SECOND STAGE		14	21-Nov-26	06-Dec-26	19-Jan-27	03-Feb-27	62,488.60	0.00	0.00	0%	0%
DAM3-C-B3-M-750	Installation of Exhaust Fans	2	21-Nov-26	22-Nov-26	19-Jan-27	20-Jan-27	7,938.56	0.00	0.00	0%	0%
DAM3-C-B3-M-780	Installation of Wall Propeller Type Exhaust Fan	4	23-Nov-26	26-Nov-26	21-Jan-27	25-Jan-27	46,831.64	0.00	0.00	0%	0%
DAM3-C-B3-M-770	Installation of Diffuser	2	02-Dec-26	03-Dec-26	31-Jan-27	01-Feb-27	2,144.00	0.00	0.00	0%	0%
DAM3-C-B3-M-960	Supply, install, test and commission door grilles & exhaust louvers	2	05-Dec-26	06-Dec-26	02-Feb-27	03-Feb-27	5,574.40	0.00	0.00	0%	0%
FIRE FIGHTING SYSTEM		26	21-Nov-26	09-Dec-26	21-Sep-26 A	07-Feb-27	102,458.78	0.00	84,594.16	0%	82.56%
FIRST STAGE		12	21-Nov-26	03-Dec-26	21-Sep-26 A	28-Sep-26 A	84,594.16	0.00	84,594.16	0%	100%
DAM3-C-B3-M-920	Installation of Fire Fighting Pipes (Seamless Black Steel)	7	21-Nov-26	28-Nov-26	21-Sep-26 A	28-Sep-26 A	72,394.75	0.00	72,394.75	0%	100%
DAM3-C-B3-M-930	Installation of Fire Fighting Valve	5	29-Nov-26	03-Dec-26	22-Sep-26 A	28-Sep-26 A	12,199.40	0.00	12,199.40	0%	100%
SECOND STAGE		17	05-Dec-26	09-Dec-26	19-Jan-27	07-Feb-27	17,864.62	0.00	0.00	0%	0%
DAM3-C-B3-M-940	Installation of Fire Hose Cabinet	3	05-Dec-26	07-Dec-26	19-Jan-27	21-Jan-27	15,158.56	0.00	0.00	0%	0%
DAM3-C-B3-M-990	Supply, install, test and commission Fire Department Connection(FDC)	3	07-Dec-26	09-Dec-26	04-Feb-27	07-Feb-27	2,706.06	0.00	0.00	0%	0%
SEWER AND DRAINAGE SYSTEM		110	12-May-26	20-Sep-26	30-Jul-26 A	07-Dec-26	90,009.74	90,009.74	30,093.94	100%	33.43%
FIRST STAGE		96	12-May-26	03-Sep-26	30-Jul-26 A	21-Nov-26	41,149.90	41,149.90	30,093.94	100%	73.13%
DAM3-C-B3-M-820	Installation of Sanitary Waste / Drainage Pipes	4	12-May-26	16-May-26	30-Jul-26 A	03-Aug-26 A	18,585.14	18,585.14	18,585.14	100%	100%
DAM3-C-B3-M-1000	Installation of Trench drain	5	30-Aug-26	03-Sep-26	08-Aug-26 A	09-Aug-26 A	11,508.80	11,508.80	11,508.80	100%	100%
DAM3-C-B3-M-840	Installation of Floor Drain	2	27-Aug-26	29-Aug-26	18-Nov-26	21-Nov-26	11,055.96	11,055.96	0.00	100%	0%
SECOND STAGE		14	05-Sep-26	20-Sep-26	21-Nov-26	07-Dec-26	48,859.84	48,859.84	0.00	100%	0%
DAM3-C-B3-M-800	Installation of Electric Water Heater	2	05-Sep-26	06-Sep-26	21-Nov-26	23-Nov-26	1,819.51	1,819.51	0.00	100%	0%
DAM3-C-B3-M-810	Installation of Sanitary Fixture and Accessories	4	07-Sep-26	10-Sep-26	23-Nov-26	28-Nov-26	19,921.72	19,921.72	0.00	100%	0%
DAM3-C-B3-M-830	Installation of Lavotary /Wash Basin	2	12-Sep-26	13-Sep-26	28-Nov-26	30-Nov-26	21,416.68	21,416.68	0.00	100%	0%
DAM3-C-B3-M-890	Installation of Bib Tap	2	14-Sep-26	15-Sep-26	30-Nov-26	02-Dec-26	1,900.66	1,900.66	0.00	100%	0%
DAM3-C-B3-M-850	Installation of Water Tap	2	16-Sep-26	17-Sep-26	02-Dec-26	05-Dec-26	2,874.14	2,874.14	0.00	100%	0%
DAM3-C-B3-M-860	Installation of Roof Vent Cap	2	19-Sep-26	20-Sep-26	05-Dec-26	07-Dec-26	927.12	927.12	0.00	100%	0%
WATER SUPPLY SYSTEM		6	21-Nov-26	02-Dec-26	01-Oct-26 A	24-Jan-27	41,870.81	0.00	41,592.68	0%	99.34%
FIRST STAGE		6	21-Nov-26	26-Nov-26	01-Oct-26 A	04-Oct-26 A	41,592.68	0.00	41,592.68	0%	100%
DAM3-C-B3-M-900	Installation of Water Supply Valve	2	25-Nov-26	26-Nov-26	01-Oct-26 A	04-Oct-26 A	18,274.27	0.00	18,274.27	0%	100%
DAM3-C-B3-M-910	Installation of Water Supply Pipes	4	21-Nov-26	24-Nov-26	01-Oct-26 A	04-Oct-26 A	23,318.41	0.00	23,318.41	0%	100%
SECOND STAGE		5	28-Nov-26	02-Dec-26	19-Jan-27	24-Jan-27	278.13	0.00	0.00	0%	0%
DAM3-C-B3-M-950	Capped connection	5	28-Nov-26	02-Dec-26	19-Jan-27	24-Jan-27	278.13	0.00	0.00	0%	0%
ELECTRICAL		166	19-Jul-26	28-Dec-26	17-Jun-26 A	20-Feb-27	752,044.76	2,920.45	20,026.20	0.39%	2.66%
FIRST STAGE		166	19-Jul-26	24-Dec-26	17-Jun-26 A	17-Feb-27	86,114.12	2,920.45	20,026.20	3.39%	23.26%
DAM3-C-B3-E-573	Installation of Earthing and Grounding	4	21-Dec-26	24-Dec-26	17-Jun-26 A	14-Feb-27	19,646.47	0.00	17,681.82	0%	90%
DAM3-C-B3-E-643	Installation of Sleeves & Power outlet	5	19-Jul-26	27-Jul-26	17-Jun-26 A	25-Oct-26	2,920.45	2,920.45	1,460.23	100%	50%
DAM3-C-B3-E-603	Installation of Conduits and wiring outlets - Fire Alarm System	4	28-Nov-26	01-Dec-26	21-Jul-26 A	27-Jan-27	1,768.31	0.00	884.15	0%	50%
DAM3-C-B3-E-623	Installation of Conduites for Lighting Fixture	4	12-Dec-26	15-Dec-26	07-Feb-27	10-Feb-27	8,462.97	0.00	0.00	0%	0%
DAM3-C-B3-E-693	Installation of Wires	2	16-Dec-26	20-Dec-26	11-Feb-27	13-Feb-27	16,925.94	0.00	0.00	0%	0%
DAM3-C-B3-E-683	Installation of LV Cables	4	21-Dec-26	24-Dec-26	14-Feb-27	17-Feb-27	36,389.98	0.00	0.00	0%	0%
SECOND STAGE		90	21-Nov-26	28-Dec-26	08-Nov-26	20-Feb-27	665,930.64	0.00	0.00	0%	0%
DAM3-C-B3-E-1040	Installation of Solar power plant	7	02-Dec-26	09-Dec-26	08-Nov-26	15-Nov-26	253,268.71	0.00	0.00	0%	0%
DAM3-C-B3-E-633	Installation of Wiring Devices	4	21-Nov-26	24-Nov-26	19-Jan-27	23-Jan-27	19,435.09	0.00	0.00	0%	0%
DAM3-C-B3-E-663	Installation of Disconnect Switches	2	25-Nov-26	26-Nov-26	24-Jan-27	25-Jan-27	30,235.95	0.00	0.00	0%	0%
DAM3-C-B3-E-583	Installation of Fire Alarm Control Panel	4	02-Dec-26	06-Dec-26	28-Jan-27	01-Feb-27	19,451.37	0.00	0.00	0%	0%
DAM3-C-B3-E-593	Installation of Fire Detectors & Accessories	4	07-Dec-26	10-Dec-26	02-Feb-27	06-Feb-27	56,740.37	0.00	0.00	0%	0%
DAM3-C-B3-E-733	Installation of Access Control System	3	12-Dec-26	16-Dec-26	07-Feb-27	09-Feb-27	27,616.86	0.00	0.00	0%	0%
DAM3-C-B3-E-743	Monitor Modules for Fire Alarm	2	17-Dec-26	19-Dec-26	10-Feb-27	11-Feb-27	3,882.38	0.00	0.00	0%	0%

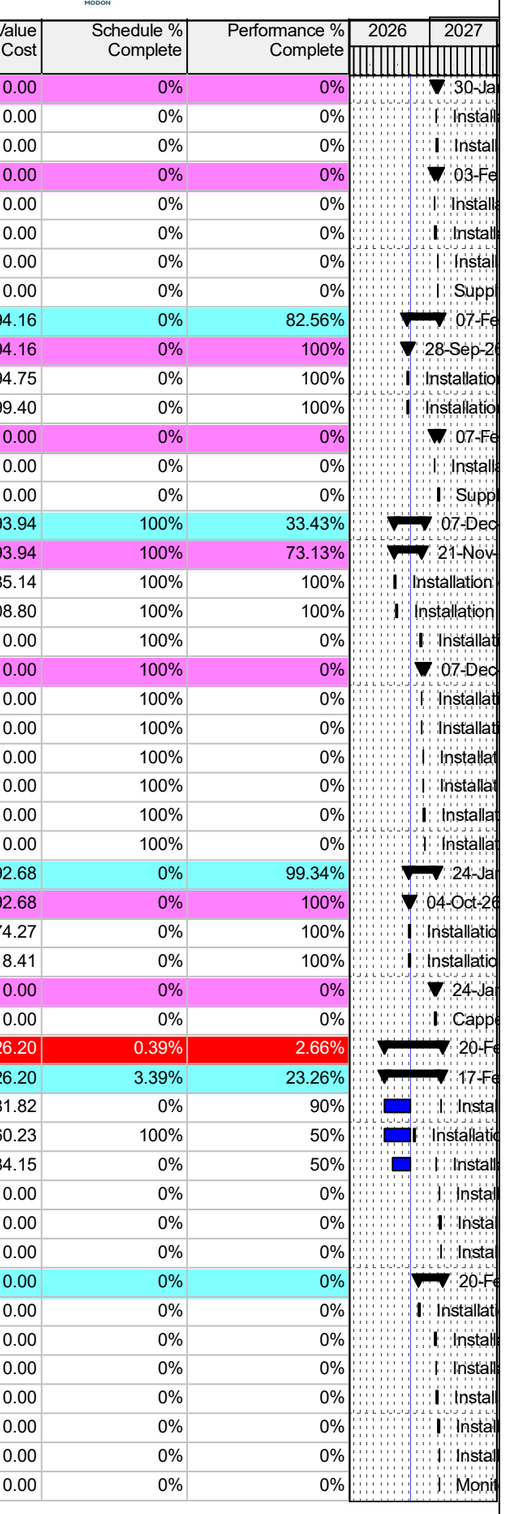

Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary

Date	Revision	Checked	Approved
06-Oct-26	Weekly Report		

Activity ID	Activity Name	Original Duration	BL Project Start	BL Project Finish	Start	Finish	Budgeted Total Cost	Planned Value Cost	Earned Value Cost	Schedule % Complete	Performance % Complete
DAM3-C-B3-E-753	Line Isolator Modules for Fire Alarm	2	20-Dec-26	21-Dec-26	13-Feb-27	14-Feb-27	185.40	0.00	0.00	0%	0%
DAM3-C-B3-E-613	Installation of Lighting fixtures	4	21-Dec-26	24-Dec-26	14-Feb-27	17-Feb-27	76,166.74	0.00	0.00	0%	0%
DAM3-C-B3-E-653	Installation of Main Distribution Board	2	21-Dec-26	22-Dec-26	14-Feb-27	15-Feb-27	32,472.73	0.00	0.00	0%	0%
DAM3-C-B3-E-763	Firewarning flash light with sounder; wall mounted, Weather proof	2	22-Dec-26	23-Dec-26	15-Feb-27	16-Feb-27	3,082.69	0.00	0.00	0%	0%
DAM3-C-B3-E-1030	Installation of CCTV System	3	23-Dec-26	28-Dec-26	16-Feb-27	18-Feb-27	76,349.24	0.00	0.00	0%	0%
DAM3-C-B3-E-703	Installation of LP-1 Panel	2	23-Dec-26	24-Dec-26	16-Feb-27	17-Feb-27	18,403.54	0.00	0.00	0%	0%
DAM3-C-B3-E-713	Installation of PP-AC panel	2	23-Dec-26	24-Dec-26	16-Feb-27	17-Feb-27	21,648.48	0.00	0.00	0%	0%
DAM3-C-B3-E-673	Installation of Telephone Cabinet	2	26-Dec-26	27-Dec-26	18-Feb-27	20-Feb-27	26,991.08	0.00	0.00	0%	0%
BLOCK B2		274	08-Mar-26	02-Jan-27	17-Feb-26 A	16-Feb-27	5,075,523.09	3,106,737.04	2,687,295.06	61.21%	52.95%
STRUCTURAL		205	08-Mar-26	29-Sep-26	17-Feb-26 A	28-Nov-26	1,389,042.53	1,389,042.53	1,388,135.41	100%	99.93%
FOOTING		43	08-Mar-26	08-Apr-26	17-Feb-26 A	13-May-26 A	597,655.16	597,655.16	597,655.16	100%	100%
DAM3-C-B2-S-150	Excavation for footings	4	08-Mar-26	11-Mar-26	17-Feb-26 A	24-Mar-26 A	89,859.61	89,859.61	89,859.61	100%	100%
DAM3-C-B2-S-6223	Soil replacement - rock fill	4	12-Mar-26	16-Mar-26	17-Mar-26 A	24-Mar-26 A	179,061.91	179,061.91	179,061.91	100%	100%
DAM3-C-B2-S-6233	Engineering fill	4	21-Mar-26	24-Mar-26	28-Mar-26 A	06-Apr-26 A	46,046.19	46,046.19	46,046.19	100%	100%
DAM3-C-B2-S-103	Lean Concrete Below Footings	2	28-Mar-26	29-Mar-26	13-Apr-26 A	13-Apr-26 A	8,229.34	8,229.34	8,229.34	100%	100%
DAM3-C-B2-S-102	Vapour Barrier for Footings	1	26-Mar-26	26-Mar-26	13-Apr-26 A	13-Apr-26 A	7,940.10	7,940.10	7,940.10	100%	100%
DAM3-C-B2-S-101	Anti Termite Below Footings	1	25-Mar-26	25-Mar-26	13-Apr-26 A	13-Apr-26 A	11,905.55	11,905.55	11,905.55	100%	100%
DAM3-C-B2-S-104	Rebar for Footings	4	30-Mar-26	02-Apr-26	06-May-26 A	11-May-26 A	101,844.98	101,844.98	101,844.98	100%	100%
DAM3-C-B2-S-105	Formwork for Footings	4	04-Apr-26	07-Apr-26	10-May-26 A	12-May-26 A	25,461.25	25,461.25	25,461.25	100%	100%
DAM3-C-B2-S-106	Pouring Concrete for Footings	1	08-Apr-26	08-Apr-26	13-May-26 A	13-May-26 A	127,306.23	127,306.23	127,306.23	100%	100%
COLUMN NECK		16	09-Apr-26	27-Apr-26	10-May-26 A	09-Jun-26 A	120,554.54	120,554.54	120,554.54	100%	100%
DAM3-C-B2-S-257	Rebar for column neck	4	09-Apr-26	13-Apr-26	10-May-26 A	12-May-26 A	14,919.19	14,919.19	14,919.19	100%	100%
DAM3-C-B2-S-267	Formwork for column neck	2	14-Apr-26	15-Apr-26	14-May-26 A	16-May-26 A	9,946.13	9,946.13	9,946.13	100%	100%
DAM3-C-B2-S-297	Pouring Concrete for column neck	1	16-Apr-26	16-Apr-26	17-May-26 A	18-May-26 A	24,865.31	24,865.31	24,865.31	100%	100%
DAM3-C-B2-S-307	Damp proof /Bitumin paint on Footings & column neck	2	18-Apr-26	19-Apr-26	19-May-26 A	20-May-26 A	24,777.73	24,777.73	24,777.73	100%	100%
DAM3-C-B2-S-367	Backfilling / Compaction up to Bottom of Grade Beams	7	20-Apr-26	27-Apr-26	24-May-26 A	09-Jun-26 A	46,046.19	46,046.19	46,046.19	100%	100%
GRADE BEAM		16	28-Apr-26	18-May-26	13-Jun-26 A	25-Jun-26 A	171,632.86	171,632.86	171,632.86	100%	100%
DAM3-C-B2-S-338	Lean Concrete Below Grade Beams	2	02-May-26	03-May-26	13-Jun-26 A	13-Jun-26 A	4,431.19	4,431.19	4,431.19	100%	100%
DAM3-C-B2-S-337	Vapour barrier for Grade Beams	2	29-Apr-26	30-Apr-26	13-Jun-26 A	13-Jun-26 A	5,293.40	5,293.40	5,293.40	100%	100%
DAM3-C-B2-S-527	Anti Termite Below Grade Beams	1	28-Apr-26	28-Apr-26	13-Jun-26 A	13-Jun-26 A	11,905.55	11,905.55	11,905.55	100%	100%
DAM3-C-B2-S-339	Rebar for Grade Beams	5	04-May-26	09-May-26	15-Jun-26 A	18-Jun-26 A	27,194.46	27,194.46	27,194.46	100%	100%
DAM3-C-B2-S-340	Formwork for Grade Beams	2	10-May-26	11-May-26	17-Jun-26 A	21-Jun-26 A	6,798.61	6,798.61	6,798.61	100%	100%
DAM3-C-B2-S-341	Anchor bolts installation	2	10-May-26	11-May-26	18-Jun-26 A	20-Jun-26 A	57,238.83	57,238.83	57,238.83	100%	100%
DAM3-C-B2-S-342	Pouring Concrete for Grade Beams	1	12-May-26	12-May-26	22-Jun-26 A	22-Jun-26 A	33,993.09	33,993.09	33,993.09	100%	100%
DAM3-C-B2-S-347	Damp proof /Bitumin paint on Grade Beams	5	13-May-26	18-May-26	24-Jun-26 A	25-Jun-26 A	24,777.73	24,777.73	24,777.73	100%	100%
SLAB ON GRADE		126	19-May-26	29-Sep-26	02-Jul-26 A	28-Nov-26	397,232.98	397,232.98	396,325.87	100%	99.77%
DAM3-C-B2-S-377	Backfilling / Compaction for Slab on Grade	7	19-May-26	30-May-26	02-Jul-26 A	06-Jul-26 A	23,023.09	23,023.09	23,023.09	100%	100%
DAM3-C-B2-S-382	Pouring Concrete for Ground Slab	4	25-Jul-26	29-Jul-26	09-Aug-26 A	10-Aug-26 A	344,195.21	344,195.21	344,195.21	100%	100%
DAM3-C-B2-S-378	Anti Termite Treatment below Ground Slab	1	04-Jun-26	04-Jun-26	09-Aug-26 A	10-Aug-26 A	15,874.08	15,874.08	15,874.08	100%	100%
DAM3-C-B2-S-379	Vapour barrier for below Ground Slab	2	06-Jun-26	07-Jun-26	09-Aug-26 A	10-Aug-26 A	13,233.49	13,233.49	13,233.49	100%	100%
DAM3-C-B2-S-517	Concrete pad	7	20-Sep-26	29-Sep-26	21-Nov-26	28-Nov-26	907.11	907.11	0.00	100%	0%
COLUMNS & BEAMS		66	31-May-26	29-Jun-26	15-Jun-26 A	04-Oct-26 A	101,966.98	101,966.98	101,966.98	100%	100%
DAM3-C-B2-S-6101	Rebar for Tie Beams	4	11-Jun-26	15-Jun-26	15-Jun-26 A	18-Jun-26 A	7,263.64	7,263.64	7,263.64	100%	100%
DAM3-C-B2-S-6102	Formwork for Tie Beams	2	16-Jun-26	17-Jun-26	17-Jun-26 A	21-Jun-26 A	1,815.91	1,815.91	1,815.91	100%	100%
DAM3-C-B2-S-6103	Pouring Concrete for Tie Beams	1	21-Jun-26	21-Jun-26	22-Jun-26 A	22-Jun-26 A	9,079.54	9,079.54	9,079.54	100%	100%
DAM3-C-B2-S-5101	Rebar for column	5	31-May-26	04-Jun-26	22-Jul-26 A	30-Jul-26 A	20,144.05	20,144.05	20,144.05	100%	100%
DAM3-C-B2-S-5102	Formwork for column	4	06-Jun-26	09-Jun-26	11-Aug-26 A	18-Aug-26 A	5,036.01	5,036.01	5,036.01	100%	100%
DAM3-C-B2-S-5103	Pouring Concrete for column	1	10-Jun-26	10-Jun-26	13-Aug-26 A	22-Aug-26 A	25,180.06	25,180.06	25,180.06	100%	100%
DAM3-C-B2-S-6113	Rebar for Beams	4	22-Jun-26	25-Jun-26	17-Sep-26 A	20-Sep-26 A	13,379.11	13,379.11	13,379.11	100%	100%

Activity ID	Activity Name	Original Duration	BL Project Start	BL Project Finish	Start	Finish	Budgeted Total Cost	Planned Value Cost	Earned Value Cost	Schedule % Complete	Performance % Complete
DAM3-C-B2-S-6123	Formwork for Beams	2	27-Jun-26	28-Jun-26	28-Sep-26 A	01-Oct-26 A	3,344.77	3,344.77	3,344.77	100%	100%
DAM3-C-B2-S-6133	Pouring Concrete for Beams	1	29-Jun-26	29-Jun-26	03-Oct-26 A	04-Oct-26 A	16,723.88	16,723.88	16,723.88	100%	100%
STRUCTURAL STEEL		63	08-Aug-26	01-Oct-26	12-Jul-26 A	03-Dec-26	1,566,668.48	1,566,668.48	1,079,035.98	100%	68.87%
DAM3-C-B2-SS-0100	Installation of columns	3	08-Aug-26	10-Aug-26	12-Jul-26 A	13-Jul-26 A	217,507.55	217,507.55	217,507.55	100%	100%
DAM3-C-B2-SS-0110	Installation of raft and purlins	5	11-Aug-26	16-Aug-26	12-Jul-26 A	14-Jul-26 A	326,261.32	326,261.32	326,261.32	100%	100%
DAM3-C-B2-SS-610	Intumescent paint to steel works	7	26-Aug-26	03-Sep-26	30-Jul-26 A	01-Aug-26 A	317,759.56	317,759.56	317,759.56	100%	100%
DAM3-C-B2-SS-0140	Installation of roof sheet	5	03-Sep-26	09-Sep-26	06-Aug-26 A	13-Aug-26 A	217,507.55	217,507.55	217,507.55	100%	100%
DAM3-C-B2-SS-620	Steel members for office area	7	03-Sep-26	12-Sep-26	12-Nov-26	19-Nov-26	115,805.20	115,805.20	0.00	100%	0%
DAM3-C-B2-SS-1020	Epoxy paint to steel members at office area	7	12-Sep-26	20-Sep-26	21-Nov-26	28-Nov-26	23,161.04	23,161.04	0.00	100%	0%
DAM3-C-B2-SS-1030	Steel members for external platform	7	12-Sep-26	20-Sep-26	21-Nov-26	28-Nov-26	18,670.78	18,670.78	0.00	100%	0%
DAM3-C-B2-SS-0130	Installation of wall sandwich panel	5	26-Sep-26	01-Oct-26	29-Nov-26	03-Dec-26	326,261.32	326,261.32	0.00	100%	0%
DAM3-C-B2-SS-1040	Epoxy paint for external platform	5	20-Sep-26	27-Sep-26	29-Nov-26	03-Dec-26	3,734.16	3,734.16	0.00	100%	0%
ARCHITECTURAL		98	17-Aug-26	02-Jan-27	12-Aug-26 A	16-Feb-27	900,244.66	122,677.48	85,409.37	13.63%	9.49%
MASONARY WORKS		19	17-Aug-26	29-Sep-26	22-Aug-26 A	27-Sep-26 A	78,954.21	78,954.21	78,954.21	100%	100%
DAM3-C-B2-A-170	Block work at toilet area	7	20-Sep-26	29-Sep-26	22-Aug-26 A	27-Sep-26 A	14,436.31	14,436.31	14,436.31	100%	100%
DAM3-C-B2-A-0120	Block work at factory area	8	17-Aug-26	27-Aug-26	22-Aug-26 A	25-Aug-26 A	58,338.72	58,338.72	58,338.72	100%	100%
DAM3-C-B2-A-0150	Block work at office area	7	12-Sep-26	20-Sep-26	22-Aug-26 A	08-Sep-26 A	6,179.18	6,179.18	6,179.18	100%	100%
WALL FINISHES		40	08-Oct-26	24-Nov-26	25-Nov-26	10-Jan-27	92,757.47	0.00	0.00	0%	0%
DAM3-C-B2-A-180	Internal Wall Plaster	15	08-Oct-26	26-Oct-26	25-Nov-26	12-Dec-26	48,590.16	0.00	0.00	0%	0%
DAM3-C-B2-A-230	Paint to Plaster (Primer, Putty & First Coat)	7	16-Nov-26	24-Nov-26	03-Jan-27	10-Jan-27	44,167.30	0.00	0.00	0%	0%
CIELING FINISHES		5	08-Nov-26	14-Nov-26	26-Dec-26	30-Dec-26	46,792.30	0.00	0.00	0%	0%
DAM3-C-B2-A-240	Installation of Ceiling Gypsum Board	5	08-Nov-26	14-Nov-26	26-Dec-26	30-Dec-26	46,792.30	0.00	0.00	0%	0%
FLOOR FINISHES		53	31-Oct-26	02-Jan-27	17-Dec-26	16-Feb-27	189,488.90	0.00	0.00	0%	0%
DAM3-C-B2-A-220	Tiles for Toilet	7	31-Oct-26	08-Nov-26	17-Dec-26	24-Dec-26	46,530.71	0.00	0.00	0%	0%
DAM3-C-B2-A-250	Tiles for Office Area	2	14-Nov-26	16-Nov-26	31-Dec-26	02-Jan-27	26,867.31	0.00	0.00	0%	0%
DAM3-C-B2-A-390	Granite strip	2	16-Nov-26	18-Nov-26	03-Jan-27	04-Jan-27	671.12	0.00	0.00	0%	0%
DAM3-C-B2-A-420	Epoxy paint	3	22-Dec-26	02-Jan-27	14-Feb-27	16-Feb-27	115,419.76	0.00	0.00	0%	0%
DOORS & WINDOWS		12	01-Oct-26	18-Oct-26	05-Dec-26	17-Dec-26	248,575.06	43,723.28	0.00	17.59%	0%
DAM3-C-B2-A-552	Window (CW1)	5	01-Oct-26	10-Oct-26	05-Dec-26	09-Dec-26	94,173.21	43,723.28	0.00	46.43%	0%
DAM3-C-B2-A-553	Roll up Shutter Door	1	10-Oct-26	11-Oct-26	10-Dec-26	10-Dec-26	68,619.20	0.00	0.00	0%	0%
DAM3-C-B2-A-200	Supply and install (D5) 1000*2200mm single leaf steel door with door	1	11-Oct-26	12-Oct-26	12-Dec-26	12-Dec-26	16,016.16	0.00	0.00	0%	0%
DAM3-C-B2-A-554	Supply and install (D4) 800*2200 mm single leaf aluminum door with door	1	12-Oct-26	13-Oct-26	13-Dec-26	13-Dec-26	22,737.85	0.00	0.00	0%	0%
DAM3-C-B2-A-555	Supply and install (D7) 1000*2200 mm single leaf aluminum door with door	1	13-Oct-26	14-Oct-26	14-Dec-26	14-Dec-26	7,811.07	0.00	0.00	0%	0%
DAM3-C-B2-A-556	Supply and install (D3) 1000*2200 mm single leaf aluminum door with door	1	14-Oct-26	15-Oct-26	15-Dec-26	15-Dec-26	16,016.16	0.00	0.00	0%	0%
DAM3-C-B2-A-557	Supply and install fire rated 45 min (D2) 1200*2200 mm single leaf steel doo	1	15-Oct-26	17-Oct-26	16-Dec-26	16-Dec-26	16,711.52	0.00	0.00	0%	0%
DAM3-C-B2-A-558	Skylight fixtures installation	1	17-Oct-26	18-Oct-26	17-Dec-26	17-Dec-26	6,489.89	0.00	0.00	0%	0%
WATER PROOFING WORKS		4	26-Oct-26	31-Oct-26	13-Dec-26	16-Dec-26	4,879.02	0.00	0.00	0%	0%
DAM3-C-B2-A-370	Waterproofing membrane for toilets	4	26-Oct-26	31-Oct-26	13-Dec-26	16-Dec-26	4,879.02	0.00	0.00	0%	0%
METAL WORKS		13	18-Nov-26	03-Dec-26	12-Aug-26 A	17-Jan-27	193,717.06	0.00	6,455.16	0%	3.33%
DAM3-C-B2-A-300	Galvanised Steel Gratings	2	01-Dec-26	03-Dec-26	12-Aug-26 A	12-Aug-26 A	6,455.16	0.00	6,455.16	0%	100%
DAM3-C-B2-A-290	Steel Ladder	2	18-Nov-26	21-Nov-26	05-Jan-27	06-Jan-27	9,839.16	0.00	0.00	0%	0%
DAM3-C-B2-A-291	Steel railing works	4	21-Nov-26	25-Nov-26	07-Jan-27	11-Jan-27	1,533.98	0.00	0.00	0%	0%
DAM3-C-B2-A-292	Aluminium composite panel	5	25-Nov-26	01-Dec-26	12-Jan-27	17-Jan-27	175,888.76	0.00	0.00	0%	0%
SPECIALTIES		23	03-Dec-26	21-Dec-26	18-Jan-27	13-Feb-27	45,080.66	0.00	0.00	0%	0%
DAM3-C-B2-A-320	Installation of fittings	5	03-Dec-26	09-Dec-26	18-Jan-27	23-Jan-27	22,981.27	0.00	0.00	0%	0%
DAM3-C-B2-A-570	Identification sign; ID01 & ID02	3	09-Dec-26	13-Dec-26	24-Jan-27	26-Jan-27	9,630.56	0.00	0.00	0%	0%
DAM3-C-B2-A-340	Furniture Installation	1	21-Dec-26	21-Dec-26	13-Feb-27	13-Feb-27	12,468.83	0.00	0.00	0%	0%
MECHANICAL		162	19-May-26	14-Dec-26	23-Jul-26 A	30-Jan-27	467,522.66	18,585.14	114,688.10	3.98%	24.53%
HVAC		14	24-Nov-26	10-Dec-26	11-Jan-27	26-Jan-27	233,183.33	0.00	0.00	0%	0%

Activity ID	Activity Name	Original Duration	BL Project Start	BL Project Finish	Start	Finish	Budgeted Total Cost	Planned Value Cost	Earned Value Cost	Schedule % Complete	Performance % Complete
FIRST STAGE		4	01-Dec-26	06-Dec-26	18-Jan-27	21-Jan-27	170,694.73	0.00	0.00	0%	0%
DAM3-C-B2-M-140	Installation of HVAC Ducts	2	01-Dec-26	03-Dec-26	18-Jan-27	19-Jan-27	149,489.33	0.00	0.00	0%	0%
DAM3-C-B2-M-170	Installation of Duct insulation	2	03-Dec-26	06-Dec-26	20-Jan-27	21-Jan-27	21,205.40	0.00	0.00	0%	0%
SECOND STAGE		14	24-Nov-26	10-Dec-26	11-Jan-27	26-Jan-27	62,488.60	0.00	0.00	0%	0%
DAM3-C-B2-M-130	Installation of Exhaust Fans	2	24-Nov-26	26-Nov-26	11-Jan-27	12-Jan-27	7,938.56	0.00	0.00	0%	0%
DAM3-C-B2-M-160	Installation of Wall Propeller Type Exhaust Fan	4	26-Nov-26	01-Dec-26	13-Jan-27	17-Jan-27	46,831.64	0.00	0.00	0%	0%
DAM3-C-B2-M-339	Installation of Diffuser	2	06-Dec-26	08-Dec-26	23-Jan-27	24-Jan-27	2,144.00	0.00	0.00	0%	0%
DAM3-C-B2-M-340	Supply, install, test and commission door grilles & exhaust louvers	2	08-Dec-26	10-Dec-26	25-Jan-27	26-Jan-27	5,574.40	0.00	0.00	0%	0%
FIRE FIGHTING SYSTEM		36	24-Nov-26	14-Dec-26	10-Sep-26 A	30-Jan-27	102,458.78	0.00	84,594.16	0%	82.56%
FIRST STAGE		12	24-Nov-26	08-Dec-26	10-Sep-26 A	21-Sep-26 A	84,594.16	0.00	84,594.16	0%	100%
DAM3-C-B2-M-300	Installation of Fire Fighting Pipes (Seamless Black Steel)	7	24-Nov-26	02-Dec-26	10-Sep-26 A	21-Sep-26 A	72,394.75	0.00	72,394.75	0%	100%
DAM3-C-B2-M-310	Installation of Fire Fighting Valve	5	02-Dec-26	08-Dec-26	10-Sep-26 A	21-Sep-26 A	12,199.40	0.00	12,199.40	0%	100%
SECOND STAGE		17	08-Dec-26	14-Dec-26	11-Jan-27	30-Jan-27	17,864.62	0.00	0.00	0%	0%
DAM3-C-B2-M-320	Installation of Fire Hose Cabinet	3	08-Dec-26	12-Dec-26	11-Jan-27	13-Jan-27	15,158.56	0.00	0.00	0%	0%
DAM3-C-B2-M-370	Supply, install, test and commission Fire Department Connection(FDC)	3	10-Dec-26	14-Dec-26	27-Jan-27	30-Jan-27	2,706.06	0.00	0.00	0%	0%
SEWER AND DRAINAGE SYSTEM		147	19-May-26	02-Dec-26	23-Jul-26 A	12-Jan-27	90,009.74	18,585.14	30,093.94	20.65%	33.43%
FIRST STAGE		133	19-May-26	16-Nov-26	23-Jul-26 A	27-Dec-26	41,149.90	18,585.14	30,093.94	45.16%	73.13%
DAM3-C-B2-M-200	Installation of Sanitary Waste / Drainage Pipes	4	19-May-26	23-May-26	23-Jul-26 A	27-Jul-26 A	18,585.14	18,585.14	18,585.14	100%	100%
DAM3-C-B2-M-380	Installation of Trench drain	5	10-Nov-26	16-Nov-26	03-Aug-26 A	04-Aug-26 A	11,508.80	0.00	11,508.80	0%	100%
DAM3-C-B2-M-220	Installation of Floor Drain	2	08-Nov-26	10-Nov-26	26-Dec-26	27-Dec-26	11,055.96	0.00	0.00	0%	0%
SECOND STAGE		14	16-Nov-26	02-Dec-26	28-Dec-26	12-Jan-27	48,859.84	0.00	0.00	0%	0%
DAM3-C-B2-M-180	Installation of Electric Water Heater	2	16-Nov-26	18-Nov-26	28-Dec-26	29-Dec-26	1,819.51	0.00	0.00	0%	0%
DAM3-C-B2-M-190	Installation of Sanitary Fixture and Accessories	4	18-Nov-26	23-Nov-26	30-Dec-26	03-Jan-27	19,921.72	0.00	0.00	0%	0%
DAM3-C-B2-M-210	Installation of Lavotary /Wash Basin	2	23-Nov-26	25-Nov-26	04-Jan-27	05-Jan-27	21,416.68	0.00	0.00	0%	0%
DAM3-C-B2-M-270	Installation of Bib Tap	2	25-Nov-26	28-Nov-26	06-Jan-27	07-Jan-27	1,900.66	0.00	0.00	0%	0%
DAM3-C-B2-M-428	Installation of Water Tap	2	28-Nov-26	30-Nov-26	09-Jan-27	10-Jan-27	2,874.14	0.00	0.00	0%	0%
DAM3-C-B2-M-429	Installation of Roof Vent Cap	2	30-Nov-26	02-Dec-26	11-Jan-27	12-Jan-27	927.12	0.00	0.00	0%	0%
WATER SUPPLY SYSTEM		11	24-Nov-26	07-Dec-26	11-Jan-27	23-Jan-27	41,870.81	0.00	0.00	0%	0%
FIRST STAGE		6	24-Nov-26	01-Dec-26	11-Jan-27	17-Jan-27	41,592.68	0.00	0.00	0%	0%
DAM3-C-B2-M-290	Installation of Water Supply Pipes	4	24-Nov-26	29-Nov-26	11-Jan-27	14-Jan-27	23,318.41	0.00	0.00	0%	0%
DAM3-C-B2-M-280	Installation of Water Supply Valve	2	29-Nov-26	01-Dec-26	16-Jan-27	17-Jan-27	18,274.27	0.00	0.00	0%	0%
SECOND STAGE		5	01-Dec-26	07-Dec-26	18-Jan-27	23-Jan-27	278.13	0.00	0.00	0%	0%
DAM3-C-B2-M-330	Capped connection	5	01-Dec-26	07-Dec-26	18-Jan-27	23-Jan-27	278.13	0.00	0.00	0%	0%
ELECTRICAL		59	29-Sep-26	21-Dec-26	17-Jun-26 A	18-Jan-27	752,044.76	9,763.41	20,026.20	1.3%	2.66%
FIRST STAGE		51	29-Sep-26	11-Nov-26	17-Jun-26 A	06-Jan-27	86,114.12	3,684.86	20,026.20	4.28%	23.26%
DAM3-C-B2-E-143	Installation of Conduits and wiring outlets - Fire Alarm System	4	29-Sep-26	04-Oct-26	17-Jun-26 A	22-Nov-26	1,768.31	1,768.31	884.15	100%	50%
DAM3-C-B2-E-113	Installation of Earthing and Grounding	5	05-Nov-26	11-Nov-26	18-Jun-26 A	06-Jan-27	19,646.47	0.00	17,681.82	0%	90%
DAM3-C-B2-E-183	Installation of Sleeves & Power outlet	8	29-Sep-26	08-Oct-26	18-Jun-26 A	24-Nov-26	2,920.45	1,916.55	1,460.23	65.63%	50%
DAM3-C-B2-E-163	Installation of Conduites for Lighting Fixture	4	13-Oct-26	18-Oct-26	02-Dec-26	06-Dec-26	8,462.97	0.00	0.00	0%	0%
DAM3-C-B2-E-233	Installation of Wires	4	18-Oct-26	22-Oct-26	19-Dec-26	22-Dec-26	16,925.94	0.00	0.00	0%	0%
DAM3-C-B2-E-223	Installation of LV Cables	4	01-Nov-26	05-Nov-26	02-Jan-27	05-Jan-27	36,389.98	0.00	0.00	0%	0%
SECOND STAGE		49	04-Oct-26	21-Dec-26	23-Nov-26	18-Jan-27	665,930.64	6,078.55	0.00	0.91%	0%
DAM3-C-B2-E-123	Installation of Fire Alarm Control Panel	4	04-Oct-26	08-Oct-26	23-Nov-26	26-Nov-26	19,451.37	6,078.55	0.00	31.25%	0%
DAM3-C-B2-E-133	Installation of Fire Detectors & Accessories	4	08-Oct-26	13-Oct-26	28-Nov-26	01-Dec-26	56,740.37	0.00	0.00	0%	0%
DAM3-C-B2-E-153	Installation of Lighting fixtures	4	22-Oct-26	27-Oct-26	23-Dec-26	27-Dec-26	76,166.74	0.00	0.00	0%	0%
DAM3-C-B2-E-193	Installation of Main Distribution Board	2	22-Oct-26	25-Oct-26	23-Dec-26	24-Dec-26	32,472.73	0.00	0.00	0%	0%
DAM3-C-B2-E-410	Installation of CCTV System	6	22-Oct-26	31-Oct-26	23-Dec-26	29-Dec-26	76,349.24	0.00	0.00	0%	0%
DAM3-C-B2-E-243	Installation of LP-1 Panel	2	25-Oct-26	27-Oct-26	26-Dec-26	27-Dec-26	18,403.54	0.00	0.00	0%	0%
DAM3-C-B2-E-253	Installation of PP-AC panel	2	27-Oct-26	29-Oct-26	28-Dec-26	29-Dec-26	21,648.48	0.00	0.00	0%	0%

Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary

Date	Revision	Checked	Approved
06-Oct-26	Weekly Report		

Activity ID	Activity Name	Original Duration	BL Project Start	BL Project Finish	Start	Finish	Budgeted Total Cost	Planned Value Cost	Earned Value Cost	Schedule % Complete	Performance % Complete
DAM3-C-B2-E-213	Installation of Telephone Cabinet	2	29-Oct-26	01-Nov-26	30-Dec-26	31-Dec-26	26,991.08	0.00	0.00	0%	0%
DAM3-C-B2-E-273	Installation of Access Control System	5	31-Oct-26	05-Nov-26	30-Dec-26	04-Jan-27	27,616.86	0.00	0.00	0%	0%
DAM3-C-B2-E-283	Monitor Modules for Fire Alarm	2	05-Nov-26	08-Nov-26	05-Jan-27	06-Jan-27	3,882.38	0.00	0.00	0%	0%
DAM3-C-B2-E-420	Installation of Solar power plant	10	10-Dec-26	21-Dec-26	06-Jan-27	18-Jan-27	253,268.71	0.00	0.00	0%	0%
DAM3-C-B2-E-293	Line Isolator Modules for Fire Alarm	2	08-Nov-26	10-Nov-26	07-Jan-27	09-Jan-27	185.40	0.00	0.00	0%	0%
DAM3-C-B2-E-303	Firewarning flash light with sounder; wall mounted, Weather proof	2	10-Nov-26	12-Nov-26	10-Jan-27	11-Jan-27	3,082.69	0.00	0.00	0%	0%
DAM3-C-B2-E-173	Installation of Wiring Devices	4	24-Nov-26	29-Nov-26	11-Jan-27	14-Jan-27	19,435.09	0.00	0.00	0%	0%
DAM3-C-B2-E-203	Installation of Disconnect Switches	2	29-Nov-26	01-Dec-26	16-Jan-27	17-Jan-27	30,235.95	0.00	0.00	0%	0%
BLOCK B1		278	12-Mar-26	03-Jan-27	17-Mar-26 A	23-Feb-27	5,075,523.09	3,291,210.87	2,667,226.41	64.84%	52.55%
STRUCTURAL		204	12-Mar-26	21-Sep-26	17-Mar-26 A	28-Nov-26	1,389,042.53	1,389,042.53	1,368,066.76	100%	98.49%
FOOTING		101	12-Mar-26	29-Apr-26	17-Mar-26 A	07-May-26 A	597,655.16	597,655.16	597,655.16	100%	100%
DAM3-C-B1-S-150	Excavation for footings	4	12-Mar-26	16-Mar-26	17-Mar-26 A	24-Mar-26 A	89,859.61	89,859.61	89,859.61	100%	100%
DAM3-C-B1-S-6243	Soil replacement - rock fill	4	21-Mar-26	24-Mar-26	17-Mar-26 A	24-Mar-26 A	179,061.91	179,061.91	179,061.91	100%	100%
DAM3-C-B1-S-6253	Engineering fill	4	25-Mar-26	29-Mar-26	07-Apr-26 A	13-Apr-26 A	46,046.19	46,046.19	46,046.19	100%	100%
DAM3-C-B1-S-103	Lean Concrete Below Footings	2	13-Apr-26	14-Apr-26	25-Apr-26 A	25-Apr-26 A	8,229.34	8,229.34	8,229.34	100%	100%
DAM3-C-B1-S-102	Vapour Barrier for Footings	1	31-Mar-26	31-Mar-26	25-Apr-26 A	25-Apr-26 A	7,940.10	7,940.10	7,940.10	100%	100%
DAM3-C-B1-S-101	Anti Termite Below Footings	1	30-Mar-26	30-Mar-26	25-Apr-26 A	25-Apr-26 A	11,905.55	11,905.55	11,905.55	100%	100%
DAM3-C-B1-S-104	Rebar for Footings	4	20-Apr-26	23-Apr-26	02-May-26 A	05-May-26 A	101,844.98	101,844.98	101,844.98	100%	100%
DAM3-C-B1-S-105	Formwork for Footings	4	25-Apr-26	28-Apr-26	05-May-26 A	06-May-26 A	25,461.25	25,461.25	25,461.25	100%	100%
DAM3-C-B1-S-106	Pouring Concrete for Footings	1	29-Apr-26	29-Apr-26	07-May-26 A	07-May-26 A	127,306.23	127,306.23	127,306.23	100%	100%
COLUMN NECK		10	30-Apr-26	18-May-26	05-May-26 A	01-Jun-26 A	120,554.54	120,554.54	120,554.54	100%	100%
DAM3-C-B1-S-257	Rebar for column neck	4	30-Apr-26	04-May-26	05-May-26 A	06-May-26 A	14,919.19	14,919.19	14,919.19	100%	100%
DAM3-C-B1-S-267	Formwork for column neck	2	05-May-26	06-May-26	11-May-26 A	12-May-26 A	9,946.13	9,946.13	9,946.13	100%	100%
DAM3-C-B1-S-297	Pouring Concrete for column neck	1	07-May-26	07-May-26	13-May-26 A	13-May-26 A	24,865.31	24,865.31	24,865.31	100%	100%
DAM3-C-B1-S-307	Damp proof /Bitumin paint on Footings & column neck	2	09-May-26	10-May-26	16-May-26 A	17-May-26 A	24,777.73	24,777.73	24,777.73	100%	100%
DAM3-C-B1-S-367	Backfilling / Compaction up to Bottom of Grade Beams	7	11-May-26	18-May-26	21-May-26 A	01-Jun-26 A	46,046.19	46,046.19	46,046.19	100%	100%
GRADE BEAM		11	19-May-26	11-Jun-26	06-Jun-26 A	25-Jun-26 A	171,632.86	171,632.86	171,632.86	100%	100%
DAM3-C-B1-S-338	Lean Concrete Below Grade Beams	2	23-May-26	24-May-26	06-Jun-26 A	06-Jun-26 A	4,431.19	4,431.19	4,431.19	100%	100%
DAM3-C-B1-S-337	Vapour barrier for Grade Beams	2	20-May-26	21-May-26	06-Jun-26 A	06-Jun-26 A	5,293.40	5,293.40	5,293.40	100%	100%
DAM3-C-B1-S-527	Anti Termite Below Grade Beams	1	19-May-26	19-May-26	06-Jun-26 A	06-Jun-26 A	11,905.55	11,905.55	11,905.55	100%	100%
DAM3-C-B1-S-339	Rebar for Grade Beams	5	25-May-26	02-Jun-26	08-Jun-26 A	09-Jun-26 A	27,194.46	27,194.46	27,194.46	100%	100%
DAM3-C-B1-S-340	Formwork for Grade Beams	2	03-Jun-26	04-Jun-26	11-Jun-26 A	15-Jun-26 A	6,798.61	6,798.61	6,798.61	100%	100%
DAM3-C-B1-S-341	Anchor bolts installation	2	03-Jun-26	04-Jun-26	11-Jun-26 A	13-Jun-26 A	57,238.83	57,238.83	57,238.83	100%	100%
DAM3-C-B1-S-342	Pouring Concrete for Grade Beams	1	06-Jun-26	06-Jun-26	17-Jun-26 A	17-Jun-26 A	33,993.09	33,993.09	33,993.09	100%	100%
DAM3-C-B1-S-347	Damp proof /Bitumin paint on Grade Beams	5	07-Jun-26	11-Jun-26	23-Jun-26 A	25-Jun-26 A	24,777.73	24,777.73	24,777.73	100%	100%
SLAB ON GRADE		119	13-Jun-26	21-Sep-26	27-Jun-26 A	28-Nov-26	397,232.98	397,232.98	396,325.87	100%	99.77%
DAM3-C-B1-S-377	Backfilling / Compaction for Slab on Grade	7	13-Jun-26	20-Jun-26	27-Jun-26 A	05-Jul-26 A	23,023.09	23,023.09	23,023.09	100%	100%
DAM3-C-B1-S-382	Pouring Concrete for Ground Slab	4	24-Jun-26	28-Jun-26	06-Aug-26 A	08-Aug-26 A	344,195.21	344,195.21	344,195.21	100%	100%
DAM3-C-B1-S-378	Anti Termite Treatment below Ground Slab	1	21-Jun-26	21-Jun-26	06-Aug-26 A	08-Aug-26 A	15,874.08	15,874.08	15,874.08	100%	100%
DAM3-C-B1-S-379	Vapour barrier for below Ground Slab	2	22-Jun-26	23-Jun-26	06-Aug-26 A	08-Aug-26 A	13,233.49	13,233.49	13,233.49	100%	100%
DAM3-C-B1-S-517	Concrete pad	7	14-Sep-26	21-Sep-26	21-Nov-26	28-Nov-26	907.11	907.11	0.00	100%	0%
COLUMNS & BEAMS		63	21-Jun-26	18-Jul-26	08-Jun-26 A	10-Oct-26	101,966.98	101,966.98	81,898.32	100%	80.32%
DAM3-C-B1-S-6101	Rebar for Tie Beams	4	02-Jul-26	06-Jul-26	08-Jun-26 A	09-Jun-26 A	7,263.64	7,263.64	7,263.64	100%	100%
DAM3-C-B1-S-6102	Formwork for Tie Beams	2	07-Jul-26	08-Jul-26	11-Jun-26 A	15-Jun-26 A	1,815.91	1,815.91	1,815.91	100%	100%
DAM3-C-B1-S-6103	Pouring Concrete for Tie Beams	1	09-Jul-26	09-Jul-26	17-Jun-26 A	17-Jun-26 A	9,079.54	9,079.54	9,079.54	100%	100%
DAM3-C-B1-S-5101	Rebar for column	5	21-Jun-26	25-Jun-26	26-Jul-26 A	28-Jul-26 A	20,144.05	20,144.05	20,144.05	100%	100%
DAM3-C-B1-S-5102	Formwork for column	4	27-Jun-26	30-Jun-26	22-Aug-26 A	27-Aug-26 A	5,036.01	5,036.01	5,036.01	100%	100%
DAM3-C-B1-S-5103	Pouring Concrete for column	1	01-Jul-26	01-Jul-26	25-Aug-26 A	29-Aug-26 A	25,180.06	25,180.06	25,180.06	100%	100%
DAM3-C-B1-S-6113	Rebar for Beams	4	11-Jul-26	14-Jul-26	27-Sep-26 A	04-Oct-26 A	13,379.11	13,379.11	13,379.11	100%	100%

Activity ID	Activity Name	Original Duration	BL Project Start	BL Project Finish	Start	Finish	Budgeted Total Cost	Planned Value Cost	Earned Value Cost	Schedule % Complete	Performance % Complete
DAM3-C-B1-S-6123	Formwork for Beams	2	15-Jul-26	16-Jul-26	06-Oct-26	08-Oct-26	3,344.77	3,344.77	0.00	100%	0%
DAM3-C-B1-S-6133	Pouring Concrete for Beams	1	18-Jul-26	18-Jul-26	08-Oct-26	10-Oct-26	16,723.88	16,723.88	0.00	100%	0%
STRUCTURAL STEEL		60	11-Aug-26	19-Sep-26	11-Jul-26 A	03-Dec-26	1,566,668.48	1,566,668.48	1,079,035.98	100%	68.87%
DAM3-C-B1-SS-0100	Installation of columns	3	11-Aug-26	13-Aug-26	11-Jul-26 A	11-Jul-26 A	217,507.55	217,507.55	217,507.55	100%	100%
DAM3-C-B1-SS-0110	Installation of raft and purlins	5	15-Aug-26	19-Aug-26	11-Jul-26 A	13-Jul-26 A	326,261.32	326,261.32	326,261.32	100%	100%
DAM3-C-B1-SS-610	Intumescent paint to steel works	7	20-Aug-26	27-Aug-26	25-Jul-26 A	28-Jul-26 A	317,759.56	317,759.56	317,759.56	100%	100%
DAM3-C-B1-SS-0140	Installation of roof sheet	5	01-Sep-26	06-Sep-26	04-Aug-26 A	11-Aug-26 A	217,507.55	217,507.55	217,507.55	100%	100%
DAM3-C-B1-SS-620	Steel members for office area	7	29-Aug-26	05-Sep-26	12-Nov-26	19-Nov-26	115,805.20	115,805.20	0.00	100%	0%
DAM3-C-B1-SS-1020	Epoxy paint to steel members at office area	7	06-Sep-26	13-Sep-26	21-Nov-26	28-Nov-26	23,161.04	23,161.04	0.00	100%	0%
DAM3-C-B1-SS-1030	Steel members for external platform	7	06-Sep-26	13-Sep-26	21-Nov-26	28-Nov-26	18,670.78	18,670.78	0.00	100%	0%
DAM3-C-B1-SS-0130	Installation of wall sandwich panel	5	14-Sep-26	19-Sep-26	29-Nov-26	03-Dec-26	326,261.32	326,261.32	0.00	100%	0%
DAM3-C-B1-SS-1040	Epoxy paint for external platform	5	14-Sep-26	19-Sep-26	29-Nov-26	03-Dec-26	3,734.16	3,734.16	0.00	100%	0%
ARCHITECTURAL		101	20-Aug-26	03-Jan-27	10-Aug-26 A	23-Feb-27	900,244.66	316,914.72	85,409.37	35.2%	9.49%
MASONARY WORKS		28	20-Aug-26	07-Oct-26	15-Aug-26 A	07-Sep-26 A	78,954.21	74,829.55	78,954.21	94.78%	100%
DAM3-C-B1-A-0120	Block work at factory area	10	20-Aug-26	31-Aug-26	15-Aug-26 A	23-Aug-26 A	58,338.72	58,338.72	58,338.72	100%	100%
DAM3-C-B1-A-0150	Block work at office area	7	06-Sep-26	13-Sep-26	23-Aug-26 A	06-Sep-26 A	6,179.18	6,179.18	6,179.18	100%	100%
DAM3-C-B1-A-170	Block work at toilet area	7	30-Sep-26	07-Oct-26	02-Sep-26 A	07-Sep-26 A	14,436.31	10,311.65	14,436.31	71.43%	100%
WALL FINISHES		45	18-Oct-26	06-Dec-26	09-Dec-26	30-Jan-27	92,757.47	0.00	0.00	0%	0%
DAM3-C-B1-A-180	Internal Wall Plaster	10	18-Oct-26	03-Nov-26	09-Dec-26	20-Dec-26	48,590.16	0.00	0.00	0%	0%
DAM3-C-B1-A-230	Paint to Plaster (Primer, Putty & First Coat)	3	29-Nov-26	06-Dec-26	27-Jan-27	30-Jan-27	44,167.30	0.00	0.00	0%	0%
CIELING FINISHES		3	21-Nov-26	25-Nov-26	30-Dec-26	02-Jan-27	46,792.30	0.00	0.00	0%	0%
DAM3-C-B1-A-240	Installation of Ceiling Gypsum Board	3	21-Nov-26	25-Nov-26	30-Dec-26	02-Jan-27	46,792.30	0.00	0.00	0%	0%
FLOOR FINISHES		51	11-Nov-26	03-Jan-27	26-Dec-26	23-Feb-27	189,488.90	0.00	0.00	0%	0%
DAM3-C-B1-A-220	Tiles for Toilet	4	11-Nov-26	18-Nov-26	26-Dec-26	29-Dec-26	46,530.71	0.00	0.00	0%	0%
DAM3-C-B1-A-250	Tiles for Office Area	2	26-Nov-26	28-Nov-26	25-Jan-27	26-Jan-27	26,867.31	0.00	0.00	0%	0%
DAM3-C-B1-A-390	Granite strip	2	29-Nov-26	30-Nov-26	27-Jan-27	28-Jan-27	671.12	0.00	0.00	0%	0%
DAM3-C-B1-A-420	Epoxy paint	7	27-Dec-26	03-Jan-27	15-Feb-27	23-Feb-27	115,419.76	0.00	0.00	0%	0%
DOORS & WINDOWS		13	20-Sep-26	28-Oct-26	05-Dec-26	19-Dec-26	248,575.06	242,085.17	0.00	97.39%	0%
DAM3-C-B1-A-552	Window (CW1)	5	20-Sep-26	28-Sep-26	05-Dec-26	09-Dec-26	94,173.21	94,173.21	0.00	100%	0%
DAM3-C-B1-A-553	Roll up Shutter Door	1	29-Sep-26	29-Sep-26	10-Dec-26	10-Dec-26	68,619.20	68,619.20	0.00	100%	0%
DAM3-C-B1-A-200	Supply and install (D5) 1000*2200mm single leaf steel door with door	1	30-Sep-26	30-Sep-26	12-Dec-26	12-Dec-26	16,016.16	16,016.16	0.00	100%	0%
DAM3-C-B1-A-554	Supply and install (D4) 800*2200 mm single leaf aluminum door with door	1	01-Oct-26	01-Oct-26	13-Dec-26	13-Dec-26	22,737.85	22,737.85	0.00	100%	0%
DAM3-C-B1-A-555	Supply and install (D7) 1000*2200 mm single leaf aluminum door with door	1	03-Oct-26	03-Oct-26	14-Dec-26	14-Dec-26	7,811.07	7,811.07	0.00	100%	0%
DAM3-C-B1-A-556	Supply and install (D3) 1000*2200 mm single leaf aluminum door with door	1	04-Oct-26	04-Oct-26	15-Dec-26	15-Dec-26	16,016.16	16,016.16	0.00	100%	0%
DAM3-C-B1-A-557	Supply and install fire rated 45 min (D2) 1200*2200 mm single leaf steel doo	1	05-Oct-26	05-Oct-26	16-Dec-26	16-Dec-26	16,711.52	16,711.52	0.00	100%	0%
DAM3-C-B1-A-558	Skylight fixtures installation	1	27-Oct-26	28-Oct-26	19-Dec-26	19-Dec-26	6,489.89	0.00	0.00	0%	0%
WATER PROOFING WORKS		4	07-Nov-26	10-Nov-26	21-Dec-26	24-Dec-26	4,879.02	0.00	0.00	0%	0%
DAM3-C-B1-A-370	Waterproofing membrane for toilets	4	07-Nov-26	10-Nov-26	21-Dec-26	24-Dec-26	4,879.02	0.00	0.00	0%	0%
METAL WORKS		7	01-Dec-26	15-Dec-26	10-Aug-26 A	06-Feb-27	193,717.06	0.00	6,455.16	0%	3.33%
DAM3-C-B1-A-300	Galvanised Steel Gratings	2	14-Dec-26	15-Dec-26	10-Aug-26 A	10-Aug-26 A	6,455.16	0.00	6,455.16	0%	100%
DAM3-C-B1-A-290	Steel Ladder	2	01-Dec-26	02-Dec-26	30-Jan-27	31-Jan-27	9,839.16	0.00	0.00	0%	0%
DAM3-C-B1-A-291	Steel railing works	2	03-Dec-26	07-Dec-26	01-Feb-27	02-Feb-27	1,533.98	0.00	0.00	0%	0%
DAM3-C-B1-A-292	Aluminium composite panel	3	08-Dec-26	13-Dec-26	03-Feb-27	06-Feb-27	175,888.76	0.00	0.00	0%	0%
SPECIALTIES		7	16-Dec-26	26-Dec-26	07-Feb-27	14-Feb-27	45,080.66	0.00	0.00	0%	0%
DAM3-C-B1-A-320	Installation of fittings	3	16-Dec-26	21-Dec-26	07-Feb-27	09-Feb-27	22,981.27	0.00	0.00	0%	0%
DAM3-C-B1-A-570	Identification sign; ID01 & ID02	3	22-Dec-26	24-Dec-26	10-Feb-27	13-Feb-27	9,630.56	0.00	0.00	0%	0%
DAM3-C-B1-A-340	Furniture Installation	1	26-Dec-26	26-Dec-26	14-Feb-27	14-Feb-27	12,468.83	0.00	0.00	0%	0%
MECHANICAL		180	13-Jun-26	26-Dec-26	18-Jul-26 A	16-Feb-27	467,522.66	18,585.14	114,688.10	3.98%	24.53%
HVAC		12	07-Dec-26	22-Dec-26	31-Jan-27	13-Feb-27	233,183.33	0.00	0.00	0%	0%

Date	Revision	Checked	Approved
06-Oct-26	Weekly Report		

Activity ID	Activity Name	Original Duration	BL Project Start	BL Project Finish	Start	Finish	Budgeted Total Cost	Planned Value Cost	Earned Value Cost	Schedule % Complete	Performance % Complete
FIRST STAGE		4	14-Dec-26	17-Dec-26	04-Feb-27	08-Feb-27	170,694.73	0.00	0.00	0%	0%
DAM3-C-B1-M-140	Installation of HVAC Ducts	2	14-Dec-26	15-Dec-26	04-Feb-27	06-Feb-27	149,489.33	0.00	0.00	0%	0%
DAM3-C-B1-M-170	Installation of Duct insulation	2	16-Dec-26	17-Dec-26	07-Feb-27	08-Feb-27	21,205.40	0.00	0.00	0%	0%
SECOND STAGE		12	07-Dec-26	22-Dec-26	31-Jan-27	13-Feb-27	62,488.60	0.00	0.00	0%	0%
DAM3-C-B1-M-130	Installation of Exhaust Fans	2	07-Dec-26	08-Dec-26	31-Jan-27	01-Feb-27	7,938.56	0.00	0.00	0%	0%
DAM3-C-B1-M-160	Installation of Wall Propeller Type Exhaust Fan	2	09-Dec-26	13-Dec-26	02-Feb-27	03-Feb-27	46,831.64	0.00	0.00	0%	0%
DAM3-C-B1-M-339	Installation of Diffuser	2	19-Dec-26	20-Dec-26	09-Feb-27	10-Feb-27	2,144.00	0.00	0.00	0%	0%
DAM3-C-B1-M-340	Supply, install, test and commission door grilles & exhaust louvers	2	21-Dec-26	22-Dec-26	11-Feb-27	13-Feb-27	5,574.40	0.00	0.00	0%	0%
FIRE FIGHTING SYSTEM		23	07-Dec-26	26-Dec-26	06-Sep-26 A	16-Feb-27	102,458.78	0.00	84,594.16	0%	82.56%
FIRST STAGE		10	07-Dec-26	20-Dec-26	06-Sep-26 A	09-Sep-26 A	84,594.16	0.00	84,594.16	0%	100%
DAM3-C-B1-M-300	Installation of Fire Fighting Pipes (Seamless Black Steel)	7	07-Dec-26	14-Dec-26	06-Sep-26 A	09-Sep-26 A	72,394.75	0.00	72,394.75	0%	100%
DAM3-C-B1-M-310	Installation of Fire Fighting Valve	5	15-Dec-26	20-Dec-26	08-Sep-26 A	09-Sep-26 A	12,199.40	0.00	12,199.40	0%	100%
SECOND STAGE		15	21-Dec-26	26-Dec-26	31-Jan-27	16-Feb-27	17,864.62	0.00	0.00	0%	0%
DAM3-C-B1-M-320	Installation of Fire Hose Cabinet	3	21-Dec-26	23-Dec-26	31-Jan-27	02-Feb-27	15,158.56	0.00	0.00	0%	0%
DAM3-C-B1-M-370	Supply, install, test and commission Fire Department Connection(FDC)	3	23-Dec-26	26-Dec-26	14-Feb-27	16-Feb-27	2,706.06	0.00	0.00	0%	0%
SEWER AND DRAINAGE SYSTEM		154	13-Jun-26	13-Dec-26	18-Jul-26 A	17-Jan-27	90,009.74	18,585.14	30,093.94	20.65%	33.43%
FIRST STAGE		140	13-Jun-26	26-Nov-26	18-Jul-26 A	31-Dec-26	41,149.90	18,585.14	30,093.94	45.16%	73.13%
DAM3-C-B1-M-200	Installation of Sanitary Waste / Drainage Pipes	4	13-Jun-26	16-Jun-26	18-Jul-26 A	25-Jul-26 A	18,585.14	18,585.14	18,585.14	100%	100%
DAM3-C-B1-M-380	Installation of Trench drain	5	22-Nov-26	26-Nov-26	19-Jul-26 A	25-Jul-26 A	11,508.80	0.00	11,508.80	0%	100%
DAM3-C-B1-M-220	Installation of Floor Drain	2	19-Nov-26	21-Nov-26	30-Dec-26	31-Dec-26	11,055.96	0.00	0.00	0%	0%
SECOND STAGE		14	28-Nov-26	13-Dec-26	02-Jan-27	17-Jan-27	48,859.84	0.00	0.00	0%	0%
DAM3-C-B1-M-180	Installation of Electric Water Heater	2	28-Nov-26	29-Nov-26	02-Jan-27	03-Jan-27	1,819.51	0.00	0.00	0%	0%
DAM3-C-B1-M-190	Installation of Sanitary Fixture and Accessories	4	30-Nov-26	03-Dec-26	04-Jan-27	07-Jan-27	19,921.72	0.00	0.00	0%	0%
DAM3-C-B1-M-210	Installation of Lavotary /Wash Basin	2	05-Dec-26	06-Dec-26	09-Jan-27	10-Jan-27	21,416.68	0.00	0.00	0%	0%
DAM3-C-B1-M-270	Installation of Bib Tap	2	07-Dec-26	08-Dec-26	11-Jan-27	12-Jan-27	1,900.66	0.00	0.00	0%	0%
DAM3-C-B1-M-428	Installation of Water Tap	2	09-Dec-26	10-Dec-26	13-Jan-27	14-Jan-27	2,874.14	0.00	0.00	0%	0%
DAM3-C-B1-M-429	Installation of Roof Vent Cap	2	12-Dec-26	13-Dec-26	16-Jan-27	17-Jan-27	927.12	0.00	0.00	0%	0%
WATER SUPPLY SYSTEM		11	07-Dec-26	19-Dec-26	31-Jan-27	11-Feb-27	41,870.81	0.00	0.00	0%	0%
FIRST STAGE		6	07-Dec-26	13-Dec-26	31-Jan-27	06-Feb-27	41,592.68	0.00	0.00	0%	0%
DAM3-C-B1-M-290	Installation of Water Supply Pipes	4	07-Dec-26	10-Dec-26	31-Jan-27	03-Feb-27	23,318.41	0.00	0.00	0%	0%
DAM3-C-B1-M-280	Installation of Water Supply Valve	2	12-Dec-26	13-Dec-26	04-Feb-27	06-Feb-27	18,274.27	0.00	0.00	0%	0%
SECOND STAGE		5	14-Dec-26	19-Dec-26	07-Feb-27	11-Feb-27	278.13	0.00	0.00	0%	0%
DAM3-C-B1-M-330	Capped connection	5	14-Dec-26	19-Dec-26	07-Feb-27	11-Feb-27	278.13	0.00	0.00	0%	0%
ELECTRICAL		78	08-Oct-26	29-Dec-26	08-Jun-26 A	06-Feb-27	752,044.76	0.00	20,026.20	0%	2.66%
FIRST STAGE		53	08-Oct-26	22-Nov-26	08-Jun-26 A	09-Jan-27	86,114.12	0.00	20,026.20	0%	23.26%
DAM3-C-B1-E-113	Installation of Earthing and Grounding	5	16-Nov-26	22-Nov-26	08-Jun-26 A	09-Jan-27	19,646.47	0.00	17,681.82	0%	90%
DAM3-C-B1-E-183	Installation of Sleeves & Power outlet	8	08-Oct-26	17-Oct-26	08-Jun-26 A	08-Dec-26	2,920.45	0.00	1,460.23	0%	50%
DAM3-C-B1-E-143	Installation of Conduits and wiring outlets - Fire Alarm System	4	08-Oct-26	12-Oct-26	09-Jun-26 A	06-Dec-26	1,768.31	0.00	884.15	0%	50%
DAM3-C-B1-E-163	Installation of Conduites for Lighting Fixture	4	22-Oct-26	26-Oct-26	16-Dec-26	20-Dec-26	8,462.97	0.00	0.00	0%	0%
DAM3-C-B1-E-233	Installation of Wires	4	28-Oct-26	02-Nov-26	21-Dec-26	24-Dec-26	16,925.94	0.00	0.00	0%	0%
DAM3-C-B1-E-223	Installation of LV Cables	4	11-Nov-26	16-Nov-26	04-Jan-27	07-Jan-27	36,389.98	0.00	0.00	0%	0%
SECOND STAGE		53	13-Oct-26	29-Dec-26	07-Dec-26	06-Feb-27	665,930.64	0.00	0.00	0%	0%
DAM3-C-B1-E-123	Installation of Fire Alarm Control Panel	4	13-Oct-26	17-Oct-26	07-Dec-26	10-Dec-26	19,451.37	0.00	0.00	0%	0%
DAM3-C-B1-E-133	Installation of Fire Detectors & Accessories	4	18-Oct-26	21-Oct-26	12-Dec-26	15-Dec-26	56,740.37	0.00	0.00	0%	0%
DAM3-C-B1-E-153	Installation of Lighting fixtures	4	02-Nov-26	07-Nov-26	26-Dec-26	29-Dec-26	76,166.74	0.00	0.00	0%	0%
DAM3-C-B1-E-193	Installation of Main Distribution Board	2	02-Nov-26	04-Nov-26	26-Dec-26	27-Dec-26	32,472.73	0.00	0.00	0%	0%
DAM3-C-B1-E-410	Installation of CCTV System	7	02-Nov-26	10-Nov-26	26-Dec-26	02-Jan-27	76,349.24	0.00	0.00	0%	0%
DAM3-C-B1-E-243	Installation of LP-1 Panel	2	04-Nov-26	07-Nov-26	28-Dec-26	29-Dec-26	18,403.54	0.00	0.00	0%	0%
DAM3-C-B1-E-253	Installation of PP-AC panel	2	07-Nov-26	09-Nov-26	30-Dec-26	31-Dec-26	21,648.48	0.00	0.00	0%	0%

2026 2027


Actual Level of Effort | Remaining Work | Milestone
Actual Work | Critical Remaining Work | summary

Date	Revision	Checked	Approved
06-Oct-26	Weekly Report		

Activity ID	Activity Name	Original Duration	BL Project Start	BL Project Finish	Start	Finish	Budgeted Total Cost	Planned Value Cost	Earned Value Cost	Schedule % Complete	Performance % Complete
DAM3-C-B1-E-213	Installation of Telephone Cabinet	2	09-Nov-26	11-Nov-26	02-Jan-27	03-Jan-27	26,991.08	0.00	0.00	0%	0%
DAM3-C-B1-E-273	Installation of Access Control System	5	10-Nov-26	16-Nov-26	03-Jan-27	07-Jan-27	27,616.86	0.00	0.00	0%	0%
DAM3-C-B1-E-283	Monitor Modules for Fire Alarm	2	16-Nov-26	18-Nov-26	09-Jan-27	10-Jan-27	3,882.38	0.00	0.00	0%	0%
DAM3-C-B1-E-293	Line Isolator Modules for Fire Alarm	2	18-Nov-26	21-Nov-26	11-Jan-27	12-Jan-27	185.40	0.00	0.00	0%	0%
DAM3-C-B1-E-303	Firewarning flash light with sounder; wall mounted, Weather proof	2	21-Nov-26	23-Nov-26	13-Jan-27	14-Jan-27	3,082.69	0.00	0.00	0%	0%
DAM3-C-B1-E-420	Installation of Solar power plant	7	22-Dec-26	29-Dec-26	18-Jan-27	26-Jan-27	253,268.71	0.00	0.00	0%	0%
DAM3-C-B1-E-173	Installation of Wiring Devices	4	07-Dec-26	10-Dec-26	31-Jan-27	03-Feb-27	19,435.09	0.00	0.00	0%	0%
DAM3-C-B1-E-203	Installation of Disconnect Switches	2	12-Dec-26	13-Dec-26	04-Feb-27	06-Feb-27	30,235.95	0.00	0.00	0%	0%
BLOCK B7		273	10-Feb-26	06-Jan-27	16-Feb-26 A	04-Jan-27	5,075,523.09	3,278,936.91	3,759,151.29	64.6%	74.06%
STRUCTURAL		212	10-Feb-26	26-Sep-26	16-Feb-26 A	19-Nov-26	1,389,042.53	1,389,042.53	1,388,135.41	100%	99.93%
FOOTING		32	10-Feb-26	25-Mar-26	16-Feb-26 A	11-Apr-26 A	597,655.16	597,655.16	597,655.16	100%	100%
DAM3-C-B7-S-150	Excavation for footings	8	10-Feb-26	19-Feb-26	16-Feb-26 A	19-Feb-26 A	89,859.61	89,859.61	89,859.61	100%	100%
DAM3-C-B7-S-6263	Soil replacement - rock fill	6	19-Feb-26	28-Feb-26	21-Feb-26 A	26-Feb-26 A	179,061.91	179,061.91	179,061.91	100%	100%
DAM3-C-B7-S-6273	Engineering fill	6	01-Mar-26	07-Mar-26	05-Mar-26 A	11-Mar-26 A	46,046.19	46,046.19	46,046.19	100%	100%
DAM3-C-B7-S-103	Lean Concrete Below Footings	2	10-Mar-26	11-Mar-26	25-Mar-26 A	25-Mar-26 A	8,229.34	8,229.34	8,229.34	100%	100%
DAM3-C-B7-S-102	Vapour Barrier for Footings	1	09-Mar-26	09-Mar-26	25-Mar-26 A	25-Mar-26 A	7,940.10	7,940.10	7,940.10	100%	100%
DAM3-C-B7-S-101	Anti Termite Below Footings	1	08-Mar-26	08-Mar-26	25-Mar-26 A	25-Mar-26 A	11,905.55	11,905.55	11,905.55	100%	100%
DAM3-C-B7-S-104	Rebar for Footings	4	12-Mar-26	16-Mar-26	05-Apr-26 A	09-Apr-26 A	101,844.98	101,844.98	101,844.98	100%	100%
DAM3-C-B7-S-105	Formwork for Footings	4	21-Mar-26	24-Mar-26	06-Apr-26 A	09-Apr-26 A	25,461.25	25,461.25	25,461.25	100%	100%
DAM3-C-B7-S-106	Pouring Concrete for Footings	1	25-Mar-26	25-Mar-26	11-Apr-26 A	11-Apr-26 A	127,306.23	127,306.23	127,306.23	100%	100%
COLUMN NECK		19	26-Mar-26	13-Apr-26	09-Apr-26 A	10-May-26 A	120,554.54	120,554.54	120,554.54	100%	100%
DAM3-C-B7-S-257	Rebar for column neck	4	26-Mar-26	30-Mar-26	09-Apr-26 A	11-Apr-26 A	14,919.19	14,919.19	14,919.19	100%	100%
DAM3-C-B7-S-267	Formwork for column neck	2	31-Mar-26	01-Apr-26	15-Apr-26 A	15-Apr-26 A	9,946.13	9,946.13	9,946.13	100%	100%
DAM3-C-B7-S-297	Pouring Concrete for column neck	1	02-Apr-26	02-Apr-26	16-Apr-26 A	16-Apr-26 A	24,865.31	24,865.31	24,865.31	100%	100%
DAM3-C-B7-S-307	Damp proof /Bitumin paint on Footings & column neck	2	04-Apr-26	05-Apr-26	20-Apr-26 A	23-Apr-26 A	24,777.73	24,777.73	24,777.73	100%	100%
DAM3-C-B7-S-367	Backfilling / Compaction up to Bottom of Grade Beams	7	06-Apr-26	13-Apr-26	02-May-26 A	10-May-26 A	46,046.19	46,046.19	46,046.19	100%	100%
GRADE BEAM		14	14-Apr-26	04-May-26	13-May-26 A	31-May-26 A	171,632.86	171,632.86	171,632.86	100%	100%
DAM3-C-B7-S-338	Lean Concrete Below Grade Beams	2	18-Apr-26	19-Apr-26	13-May-26 A	13-May-26 A	4,431.19	4,431.19	4,431.19	100%	100%
DAM3-C-B7-S-337	Vapour barrier for Grade Beams	2	15-Apr-26	16-Apr-26	13-May-26 A	13-May-26 A	5,293.40	5,293.40	5,293.40	100%	100%
DAM3-C-B7-S-527	Anti Termite Below Grade Beams	1	14-Apr-26	14-Apr-26	13-May-26 A	13-May-26 A	11,905.55	11,905.55	11,905.55	100%	100%
DAM3-C-B7-S-339	Rebar for Grade Beams	5	20-Apr-26	25-Apr-26	16-May-26 A	18-May-26 A	27,194.46	27,194.46	27,194.46	100%	100%
DAM3-C-B7-S-341	Anchor bolts installation	2	26-Apr-26	27-Apr-26	16-May-26 A	18-May-26 A	57,238.83	57,238.83	57,238.83	100%	100%
DAM3-C-B7-S-340	Formwork for Grade Beams	2	26-Apr-26	27-Apr-26	18-May-26 A	19-May-26 A	6,798.61	6,798.61	6,798.61	100%	100%
DAM3-C-B7-S-342	Pouring Concrete for Grade Beams	1	28-Apr-26	28-Apr-26	20-May-26 A	20-May-26 A	33,993.09	33,993.09	33,993.09	100%	100%
DAM3-C-B7-S-347	Damp proof /Bitumin paint on Grade Beams	5	29-Apr-26	04-May-26	23-May-26 A	31-May-26 A	24,777.73	24,777.73	24,777.73	100%	100%
SLAB ON GRADE		143	05-May-26	26-Sep-26	01-Jun-26 A	19-Nov-26	397,232.98	397,232.98	396,325.87	100%	99.77%
DAM3-C-B7-S-377	Backfilling / Compaction for Slab on Grade	7	05-May-26	12-May-26	01-Jun-26 A	08-Jun-26 A	23,023.09	23,023.09	23,023.09	100%	100%
DAM3-C-B7-S-382	Pouring Concrete for Ground Slab	4	17-May-26	20-May-26	08-Jul-26 A	12-Jul-26 A	344,195.21	344,195.21	344,195.21	100%	100%
DAM3-C-B7-S-378	Anti Termite Treatment below Ground Slab	1	13-May-26	13-May-26	08-Jul-26 A	12-Jul-26 A	15,874.08	15,874.08	15,874.08	100%	100%
DAM3-C-B7-S-379	Vapour barrier for below Ground Slab	2	14-May-26	16-May-26	08-Jul-26 A	12-Jul-26 A	13,233.49	13,233.49	13,233.49	100%	100%
DAM3-C-B7-S-517	Concrete pad	7	17-Sep-26	26-Sep-26	12-Nov-26	19-Nov-26	907.11	907.11	0.00	100%	0%
COLUMNS & BEAMS		58	13-May-26	13-Jun-26	11-May-26 A	29-Aug-26 A	101,966.98	101,966.98	101,966.98	100%	100%
DAM3-C-B7-S-6101	Rebar for Tie Beams	4	25-May-26	01-Jun-26	11-May-26 A	12-May-26 A	7,263.64	7,263.64	7,263.64	100%	100%
DAM3-C-B7-S-6102	Formwork for Tie Beams	2	02-Jun-26	03-Jun-26	13-May-26 A	13-May-26 A	1,815.91	1,815.91	1,815.91	100%	100%
DAM3-C-B7-S-6103	Pouring Concrete for Tie Beams	1	04-Jun-26	04-Jun-26	14-May-26 A	14-May-26 A	9,079.54	9,079.54	9,079.54	100%	100%
DAM3-C-B7-S-5102	Formwork for column	4	19-May-26	23-May-26	01-Jun-26 A	07-Jul-26 A	5,036.01	5,036.01	5,036.01	100%	100%
DAM3-C-B7-S-5101	Rebar for column	5	13-May-26	18-May-26	25-Jun-26 A	02-Jul-26 A	20,144.05	20,144.05	20,144.05	100%	100%
DAM3-C-B7-S-5103	Pouring Concrete for column	1	24-May-26	24-May-26	05-Jul-26 A	22-Jul-26 A	25,180.06	25,180.06	25,180.06	100%	100%
DAM3-C-B7-S-6113	Rebar for Beams	4	06-Jun-26	09-Jun-26	16-Aug-26 A	19-Aug-26 A	13,379.11	13,379.11	13,379.11	100%	100%

Activity ID	Activity Name	Original Duration	BL Project Start	BL Project Finish	Start	Finish	Budgeted Total Cost	Planned Value Cost	Earned Value Cost	Schedule % Complete	Performance % Complete
DAM3-C-B7-S-6123	Formwork for Beams	2	10-Jun-26	11-Jun-26	20-Aug-26 A	26-Aug-26 A	3,344.77	3,344.77	3,344.77	100%	100%
DAM3-C-B7-S-6133	Pouring Concrete for Beams	1	13-Jun-26	13-Jun-26	26-Aug-26 A	29-Aug-26 A	16,723.88	16,723.88	16,723.88	100%	100%
STRUCTURAL STEEL		41	15-Aug-26	22-Sep-26	13-Jun-26 A	19-Nov-26	1,566,668.48	1,566,668.48	1,539,773.29	100%	98.28%
DAM3-C-B7-SS-0100	Installation of columns	3	15-Aug-26	17-Aug-26	13-Jun-26 A	13-Jun-26 A	217,507.55	217,507.55	217,507.55	100%	100%
DAM3-C-B7-SS-0110	Installation of raft and purlins	5	18-Aug-26	23-Aug-26	14-Jun-26 A	15-Jun-26 A	326,261.32	326,261.32	326,261.32	100%	100%
DAM3-C-B7-SS-610	Intumescent paint to steel works	7	24-Aug-26	31-Aug-26	14-Jun-26 A	21-Jun-26 A	317,759.56	317,759.56	317,759.56	100%	100%
DAM3-C-B7-SS-0140	Installation of roof sheet	5	05-Sep-26	09-Sep-26	07-Jul-26 A	25-Jul-26 A	217,507.55	217,507.55	217,507.55	100%	100%
DAM3-C-B7-SS-1030	Steel members for external platform	7	09-Sep-26	16-Sep-26	24-Aug-26 A	19-Sep-26 A	18,670.78	18,670.78	18,670.78	100%	100%
DAM3-C-B7-SS-0130	Installation of wall sandwich panel	5	17-Sep-26	22-Sep-26	01-Sep-26 A	24-Sep-26 A	326,261.32	326,261.32	326,261.32	100%	100%
DAM3-C-B7-SS-620	Steel members for office area	7	01-Sep-26	08-Sep-26	21-Sep-26 A	24-Sep-26 A	115,805.20	115,805.20	115,805.20	100%	100%
DAM3-C-B7-SS-1020	Epoxy paint to steel members at office area	7	09-Sep-26	16-Sep-26	12-Nov-26	19-Nov-26	23,161.04	23,161.04	0.00	100%	0%
DAM3-C-B7-SS-1040	Epoxy paint for external platform	5	17-Sep-26	22-Sep-26	12-Nov-26	17-Nov-26	3,734.16	3,734.16	0.00	100%	0%
ARCHITECTURAL		81	24-Aug-26	19-Dec-26	01-Jul-26 A	04-Jan-27	900,244.66	280,500.63	296,455.53	31.16%	32.93%
MASONARY WORKS		23	24-Aug-26	26-Sep-26	22-Jul-26 A	17-Aug-26 A	78,954.21	78,954.21	78,954.21	100%	100%
DAM3-C-B7-A-0120	Block work at factory area	10	24-Aug-26	03-Sep-26	22-Jul-26 A	26-Jul-26 A	58,338.72	58,338.72	58,338.72	100%	100%
DAM3-C-B7-A-0150	Block work at office area	7	09-Sep-26	16-Sep-26	25-Jul-26 A	17-Aug-26 A	6,179.18	6,179.18	6,179.18	100%	100%
DAM3-C-B7-A-170	Block work at toilet area	7	17-Sep-26	26-Sep-26	26-Jul-26 A	17-Aug-26 A	14,436.31	14,436.31	14,436.31	100%	100%
WALL FINISHES		15	06-Oct-26	21-Nov-26	03-Sep-26 A	03-Dec-26	92,757.47	0.00	81,715.64	0%	88.1%
DAM3-C-B7-A-180	Internal Wall Plaster	15	06-Oct-26	22-Oct-26	03-Sep-26 A	24-Sep-26 A	48,590.16	0.00	48,590.16	0%	100%
DAM3-C-B7-A-230	Paint to Plaster (Primer, Putty & First Coat)	4	14-Nov-26	21-Nov-26	28-Sep-26 A	03-Dec-26	44,167.30	0.00	33,125.48	0%	75%
CIELING FINISHES		5	05-Nov-26	10-Nov-26	25-Nov-26	30-Nov-26	46,792.30	0.00	0.00	0%	0%
DAM3-C-B7-A-240	Installation of Ceiling Gypsum Board	5	05-Nov-26	10-Nov-26	25-Nov-26	30-Nov-26	46,792.30	0.00	0.00	0%	0%
FLOOR FINISHES		37	28-Oct-26	19-Dec-26	19-Sep-26 A	04-Jan-27	189,488.90	0.00	46,530.71	0%	24.56%
DAM3-C-B7-A-220	Tiles for Toilet	7	28-Oct-26	04-Nov-26	19-Sep-26 A	28-Sep-26 A	46,530.71	0.00	46,530.71	0%	100%
DAM3-C-B7-A-250	Tiles for Office Area	2	11-Nov-26	12-Nov-26	01-Dec-26	02-Dec-26	26,867.31	0.00	0.00	0%	0%
DAM3-C-B7-A-390	Granite strip	2	14-Nov-26	15-Nov-26	03-Dec-26	06-Dec-26	671.12	0.00	0.00	0%	0%
DAM3-C-B7-A-420	Epoxy paint	7	12-Dec-26	19-Dec-26	27-Dec-26	04-Jan-27	115,419.76	0.00	0.00	0%	0%
DOORS & WINDOWS		11	24-Sep-26	10-Oct-26	21-Sep-26 A	03-Dec-26	248,575.06	201,546.42	30,033.19	81.08%	12.08%
DAM3-C-B7-A-558	Skylight fixtures installation	1	10-Oct-26	10-Oct-26	21-Sep-26 A	26-Sep-26 A	6,489.89	0.00	6,489.89	0%	100%
DAM3-C-B7-A-552	Window (CW1)	7	24-Sep-26	01-Oct-26	05-Oct-26 A	26-Nov-26	94,173.21	94,173.21	23,543.30	100%	25%
DAM3-C-B7-A-553	Roll up Shutter Door	1	03-Oct-26	03-Oct-26	26-Nov-26	28-Nov-26	68,619.20	68,619.20	0.00	100%	0%
DAM3-C-B7-A-200	Supply and install (D5) 1000*2200mm single leaf steel door with door	1	04-Oct-26	04-Oct-26	28-Nov-26	29-Nov-26	16,016.16	16,016.16	0.00	100%	0%
DAM3-C-B7-A-554	Supply and install (D4) 800*2200 mm single leaf aluminum door with door	1	05-Oct-26	05-Oct-26	29-Nov-26	30-Nov-26	22,737.85	22,737.85	0.00	100%	0%
DAM3-C-B7-A-555	Supply and install (D7) 1000*2200 mm single leaf aluminum door with door	1	06-Oct-26	06-Oct-26	30-Nov-26	01-Dec-26	7,811.07	0.00	0.00	0%	0%
DAM3-C-B7-A-556	Supply and install (D3) 1000*2200 mm single leaf aluminum door with door	1	07-Oct-26	07-Oct-26	01-Dec-26	02-Dec-26	16,016.16	0.00	0.00	0%	0%
DAM3-C-B7-A-557	Supply and install fire rated 45 min (D2) 1200*2200 mm single leaf steel doo	1	08-Oct-26	08-Oct-26	02-Dec-26	03-Dec-26	16,711.52	0.00	0.00	0%	0%
WATER PROOFING WORKS		4	24-Oct-26	27-Oct-26	21-Nov-26	24-Nov-26	4,879.02	0.00	0.00	0%	0%
DAM3-C-B7-A-370	Waterproofing membrane for toilets	4	24-Oct-26	27-Oct-26	21-Nov-26	24-Nov-26	4,879.02	0.00	0.00	0%	0%
METAL WORKS		20	16-Nov-26	30-Nov-26	01-Jul-26 A	16-Dec-26	193,717.06	0.00	59,221.79	0%	30.57%
DAM3-C-B7-A-300	Galvanised Steel Gratings	2	29-Nov-26	30-Nov-26	01-Jul-26 A	01-Jul-26 A	6,455.16	0.00	6,455.16	0%	100%
DAM3-C-B7-A-292	Aluminium composite panel	5	23-Nov-26	28-Nov-26	30-Sep-26 A	16-Dec-26	175,888.76	0.00	52,766.63	0%	30%
DAM3-C-B7-A-290	Steel Ladder	2	16-Nov-26	17-Nov-26	06-Dec-26	08-Dec-26	9,839.16	0.00	0.00	0%	0%
DAM3-C-B7-A-291	Steel railing works	4	18-Nov-26	22-Nov-26	08-Dec-26	13-Dec-26	1,533.98	0.00	0.00	0%	0%
SPECIALTIES		9	01-Dec-26	10-Dec-26	16-Dec-26	27-Dec-26	45,080.66	0.00	0.00	0%	0%
DAM3-C-B7-A-320	Installation of fittings	5	01-Dec-26	06-Dec-26	16-Dec-26	22-Dec-26	22,981.27	0.00	0.00	0%	0%
DAM3-C-B7-A-570	Identification sign; ID01 & ID02	3	07-Dec-26	09-Dec-26	22-Dec-26	26-Dec-26	9,630.56	0.00	0.00	0%	0%
DAM3-C-B7-A-340	Furniture Installation	1	10-Dec-26	10-Dec-26	26-Dec-26	27-Dec-26	12,468.83	0.00	0.00	0%	0%
MECHANICAL		178	05-May-26	10-Dec-26	10-Jun-26 A	21-Dec-26	467,522.66	18,585.14	231,025.45	3.98%	49.41%
HVAC		12	22-Nov-26	07-Dec-26	05-Oct-26 A	17-Dec-26	233,183.33	0.00	74,744.66	0%	32.05%

Activity ID	Activity Name	Original Duration	BL Project Start	BL Project Finish	Start	Finish	Budgeted Total Cost	Planned Value Cost	Earned Value Cost	Schedule % Complete	Performance % Complete
FIRST STAGE		3	29-Nov-26	02-Dec-26	05-Oct-26 A	13-Dec-26	170,694.73	0.00	74,744.66	0%	43.79%
DAM3-C-B7-M-140	Installation of HVAC Ducts	2	29-Nov-26	30-Nov-26	05-Oct-26 A	10-Dec-26	149,489.33	0.00	74,744.66	0%	50%
DAM3-C-B7-M-170	Installation of Duct insulation	2	01-Dec-26	02-Dec-26	12-Dec-26	13-Dec-26	21,205.40	0.00	0.00	0%	0%
SECOND STAGE		12	22-Nov-26	07-Dec-26	05-Dec-26	17-Dec-26	62,488.60	0.00	0.00	0%	0%
DAM3-C-B7-M-130	Installation of Exhaust Fans	2	22-Nov-26	23-Nov-26	05-Dec-26	06-Dec-26	7,938.56	0.00	0.00	0%	0%
DAM3-C-B7-M-160	Installation of Wall Propeller Type Exhaust Fan	3	24-Nov-26	28-Nov-26	07-Dec-26	09-Dec-26	46,831.64	0.00	0.00	0%	0%
DAM3-C-B7-M-339	Installation of Diffuser	2	03-Dec-26	05-Dec-26	14-Dec-26	15-Dec-26	2,144.00	0.00	0.00	0%	0%
DAM3-C-B7-M-340	Supply, install, test and commission door grilles & exhaust louvers	2	06-Dec-26	07-Dec-26	16-Dec-26	17-Dec-26	5,574.40	0.00	0.00	0%	0%
FIRE FIGHTING SYSTEM		29	22-Nov-26	10-Dec-26	29-Jul-26 A	21-Dec-26	102,458.78	0.00	84,594.16	0%	82.56%
FIRST STAGE		17	22-Nov-26	05-Dec-26	29-Jul-26 A	12-Aug-26 A	84,594.16	0.00	84,594.16	0%	100%
DAM3-C-B7-M-300	Installation of Fire Fighting Pipes (Seamless Black Steel)	7	22-Nov-26	29-Nov-26	29-Jul-26 A	10-Aug-26 A	72,394.75	0.00	72,394.75	0%	100%
DAM3-C-B7-M-310	Installation of Fire Fighting Valve	5	30-Nov-26	05-Dec-26	09-Aug-26 A	12-Aug-26 A	12,199.40	0.00	12,199.40	0%	100%
SECOND STAGE		15	06-Dec-26	10-Dec-26	05-Dec-26	21-Dec-26	17,864.62	0.00	0.00	0%	0%
DAM3-C-B7-M-320	Installation of Fire Hose Cabinet	3	06-Dec-26	08-Dec-26	05-Dec-26	07-Dec-26	15,158.56	0.00	0.00	0%	0%
DAM3-C-B7-M-370	Supply, install, test and commission Fire Department Connection(FDC)	3	08-Dec-26	10-Dec-26	19-Dec-26	21-Dec-26	2,706.06	0.00	0.00	0%	0%
SEWER AND DRAINAGE SYSTEM		153	05-May-26	29-Nov-26	10-Jun-26 A	13-Dec-26	90,009.74	18,585.14	30,093.94	20.65%	33.43%
FIRST STAGE		153	05-May-26	12-Nov-26	10-Jun-26 A	26-Nov-26	41,149.90	18,585.14	30,093.94	45.16%	73.13%
DAM3-C-B7-M-200	Installation of Sanitary Waste / Drainage Pipes	4	05-May-26	09-May-26	10-Jun-26 A	14-Jun-26 A	18,585.14	18,585.14	18,585.14	100%	100%
DAM3-C-B7-M-380	Installation of Trench drain	5	08-Nov-26	12-Nov-26	16-Jun-26 A	18-Jun-26 A	11,508.80	0.00	11,508.80	0%	100%
DAM3-C-B7-M-220	Installation of Floor Drain	2	05-Nov-26	07-Nov-26	25-Nov-26	26-Nov-26	11,055.96	0.00	0.00	0%	0%
SECOND STAGE		14	14-Nov-26	29-Nov-26	28-Nov-26	13-Dec-26	48,859.84	0.00	0.00	0%	0%
DAM3-C-B7-M-180	Installation of Electric Water Heater	2	14-Nov-26	15-Nov-26	28-Nov-26	29-Nov-26	1,819.51	0.00	0.00	0%	0%
DAM3-C-B7-M-190	Installation of Sanitary Fixture and Accessories	4	16-Nov-26	19-Nov-26	30-Nov-26	03-Dec-26	19,921.72	0.00	0.00	0%	0%
DAM3-C-B7-M-210	Installation of Lavotary /Wash Basin	2	21-Nov-26	22-Nov-26	05-Dec-26	06-Dec-26	21,416.68	0.00	0.00	0%	0%
DAM3-C-B7-M-270	Installation of Bib Tap	2	23-Nov-26	24-Nov-26	07-Dec-26	08-Dec-26	1,900.66	0.00	0.00	0%	0%
DAM3-C-B7-M-428	Installation of Water Tap	2	25-Nov-26	26-Nov-26	09-Dec-26	10-Dec-26	2,874.14	0.00	0.00	0%	0%
DAM3-C-B7-M-429	Installation of Roof Vent Cap	2	28-Nov-26	29-Nov-26	12-Dec-26	13-Dec-26	927.12	0.00	0.00	0%	0%
WATER SUPPLY SYSTEM		33	22-Nov-26	03-Dec-26	30-Aug-26 A	09-Dec-26	41,870.81	0.00	41,592.68	0%	99.34%
FIRST STAGE		9	22-Nov-26	28-Nov-26	30-Aug-26 A	03-Sep-26 A	41,592.68	0.00	41,592.68	0%	100%
DAM3-C-B7-M-290	Installation of Water Supply Pipes	4	22-Nov-26	25-Nov-26	30-Aug-26 A	03-Sep-26 A	23,318.41	0.00	23,318.41	0%	100%
DAM3-C-B7-M-280	Installation of Water Supply Valve	2	26-Nov-26	28-Nov-26	31-Aug-26 A	03-Sep-26 A	18,274.27	0.00	18,274.27	0%	100%
SECOND STAGE		5	29-Nov-26	03-Dec-26	05-Dec-26	09-Dec-26	278.13	0.00	0.00	0%	0%
DAM3-C-B7-M-330	Capped connection	5	29-Nov-26	03-Dec-26	05-Dec-26	09-Dec-26	278.13	0.00	0.00	0%	0%
ELECTRICAL		67	27-Sep-26	06-Jan-27	16-May-26 A	29-Dec-26	752,044.76	24,140.13	303,761.61	3.21%	40.39%
FIRST STAGE		63	27-Sep-26	08-Nov-26	16-May-26 A	22-Dec-26	86,114.12	4,688.76	27,642.87	5.44%	32.1%
DAM3-C-B7-E-113	Installation of Earthing and Grounding	5	03-Nov-26	08-Nov-26	16-May-26 A	22-Dec-26	19,646.47	0.00	17,681.82	0%	90%
DAM3-C-B7-E-143	Installation of Conduits and wiring outlets - Fire Alarm System	4	27-Sep-26	30-Sep-26	16-May-26 A	14-Nov-26	1,768.31	1,768.31	884.15	100%	50%
DAM3-C-B7-E-183	Installation of Sleeves & Power outlet	8	27-Sep-26	05-Oct-26	18-May-26 A	16-Nov-26	2,920.45	2,920.45	1,460.23	100%	50%
DAM3-C-B7-E-163	Installation of Conduites for Lighting Fixture	4	11-Oct-26	14-Oct-26	06-Sep-26 A	24-Nov-26	8,462.97	0.00	7,616.67	0%	90%
DAM3-C-B7-E-233	Installation of Wires	4	15-Oct-26	19-Oct-26	03-Dec-26	08-Dec-26	16,925.94	0.00	0.00	0%	0%
DAM3-C-B7-E-223	Installation of LV Cables	4	29-Oct-26	02-Nov-26	17-Dec-26	22-Dec-26	36,389.98	0.00	0.00	0%	0%
SECOND STAGE		67	01-Oct-26	06-Jan-27	21-Sep-26 A	29-Dec-26	665,930.64	19,451.37	276,118.73	2.92%	41.46%
DAM3-C-B7-E-153	Installation of Lighting fixtures	4	20-Oct-26	24-Oct-26	21-Sep-26 A	12-Dec-26	76,166.74	0.00	22,850.02	0%	30%
DAM3-C-B7-E-420	Installation of Solar power plant	7	30-Dec-26	06-Jan-27	04-Oct-26 A	06-Oct-26 A	253,268.71	0.00	253,268.71	0%	100%
DAM3-C-B7-E-123	Installation of Fire Alarm Control Panel	4	01-Oct-26	05-Oct-26	15-Nov-26	18-Nov-26	19,451.37	19,451.37	0.00	100%	0%
DAM3-C-B7-E-133	Installation of Fire Detectors & Accessories	4	06-Oct-26	10-Oct-26	19-Nov-26	23-Nov-26	56,740.37	0.00	0.00	0%	0%
DAM3-C-B7-E-173	Installation of Wiring Devices	4	22-Nov-26	25-Nov-26	05-Dec-26	08-Dec-26	19,435.09	0.00	0.00	0%	0%
DAM3-C-B7-E-193	Installation of Main Distribution Board	2	20-Oct-26	21-Oct-26	08-Dec-26	10-Dec-26	32,472.73	0.00	0.00	0%	0%
DAM3-C-B7-E-410	Installation of CCTV System	7	20-Oct-26	27-Oct-26	08-Dec-26	16-Dec-26	76,349.24	0.00	0.00	0%	0%

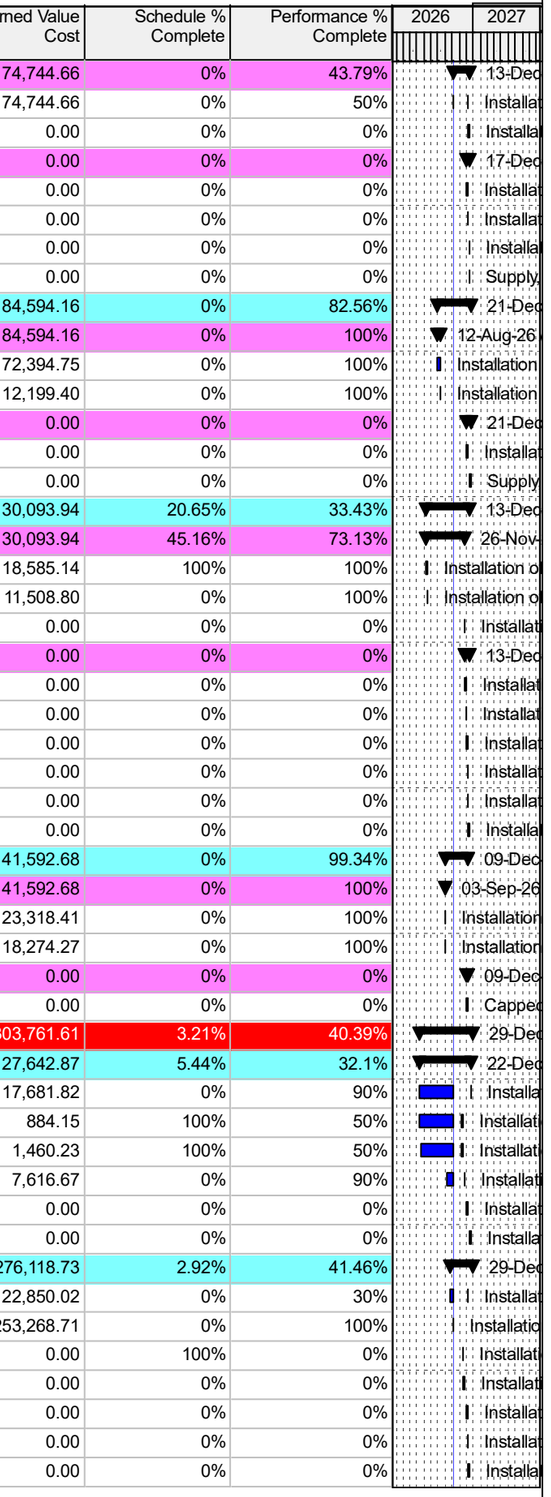

Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary

Date	Revision	Checked	Approved
06-Oct-26	Weekly Report		

Activity ID	Activity Name	Original Duration	BL Project Start	BL Project Finish	Start	Finish	Budgeted Total Cost	Planned Value Cost	Earned Value Cost	Schedule % Complete	Performance % Complete	2026	2027
DAM3-C-B7-E-203	Installation of Disconnect Switches	2	26-Nov-26	28-Nov-26	09-Dec-26	10-Dec-26	30,235.95	0.00	0.00	0%	0%	Installat	
DAM3-C-B7-E-243	Installation of LP-1 Panel	2	22-Oct-26	24-Oct-26	10-Dec-26	13-Dec-26	18,403.54	0.00	0.00	0%	0%	Installa	
DAM3-C-B7-E-253	Installation of PP-AC panel	2	25-Oct-26	26-Oct-26	13-Dec-26	15-Dec-26	21,648.48	0.00	0.00	0%	0%	Installa	
DAM3-C-B7-E-213	Installation of Telephone Cabinet	2	27-Oct-26	28-Oct-26	15-Dec-26	17-Dec-26	26,991.08	0.00	0.00	0%	0%	Installa	
DAM3-C-B7-E-273	Installation of Access Control System	5	28-Oct-26	02-Nov-26	16-Dec-26	22-Dec-26	27,616.86	0.00	0.00	0%	0%	Installa	
DAM3-C-B7-E-283	Monitor Modules for Fire Alarm	2	03-Nov-26	04-Nov-26	22-Dec-26	24-Dec-26	3,882.38	0.00	0.00	0%	0%	Monito	
DAM3-C-B7-E-293	Line Isolator Modules for Fire Alarm	2	05-Nov-26	07-Nov-26	24-Dec-26	27-Dec-26	185.40	0.00	0.00	0%	0%	Line Is	
DAM3-C-B7-E-303	Firewarning flash light with sounder; wall mounted, Weather proof	2	08-Nov-26	09-Nov-26	27-Dec-26	29-Dec-26	3,082.69	0.00	0.00	0%	0%	Firewa	
BLOCK B8		292	19-Feb-26	14-Jan-27	17-Feb-26 A	28-Feb-27	5,075,523.09	2,687,335.31	3,320,936.13	52.95%	65.43%	28-F	
STRUCTURAL		208	19-Feb-26	17-Oct-26	17-Feb-26 A	19-Nov-26	1,389,042.53	1,388,135.41	1,388,135.41	99.93%	99.93%	19-Nov-	
FOOTING		58	19-Feb-26	13-May-26	17-Feb-26 A	16-Apr-26 A	597,655.16	597,655.16	597,655.16	100%	100%	16-Apr-26 A, F	
DAM3-C-B8-S-150	Excavation for footings	4	19-Feb-26	25-Feb-26	17-Feb-26 A	21-Feb-26 A	89,859.61	89,859.61	89,859.61	100%	100%	Excavation for fo	
DAM3-C-B8-S-6283	Soil replacement - rock fill	4	25-Feb-26	02-Mar-26	28-Feb-26 A	02-Mar-26 A	179,061.91	179,061.91	179,061.91	100%	100%	Soil replacemen	
DAM3-C-B8-S-6293	Engineering fill	4	03-Mar-26	07-Mar-26	08-Mar-26 A	16-Mar-26 A	46,046.19	46,046.19	46,046.19	100%	100%	Engineering fill	
DAM3-C-B8-S-103	Lean Concrete Below Footings	2	10-Mar-26	11-Mar-26	28-Mar-26 A	28-Mar-26 A	8,229.34	8,229.34	8,229.34	100%	100%	Lean Concrete	
DAM3-C-B8-S-102	Vapour Barrier for Footings	1	09-Mar-26	09-Mar-26	28-Mar-26 A	28-Mar-26 A	7,940.10	7,940.10	7,940.10	100%	100%	Vapour Barrier f	
DAM3-C-B8-S-101	Anti Termite Below Footings	1	08-Mar-26	08-Mar-26	28-Mar-26 A	28-Mar-26 A	11,905.55	11,905.55	11,905.55	100%	100%	Anti Termite Be	
DAM3-C-B8-S-104	Rebar for Footings	4	12-Mar-26	16-Mar-26	11-Apr-26 A	13-Apr-26 A	101,844.98	101,844.98	101,844.98	100%	100%	Rebar for Foot	
DAM3-C-B8-S-105	Formwork for Footings	4	09-May-26	12-May-26	13-Apr-26 A	14-Apr-26 A	25,461.25	25,461.25	25,461.25	100%	100%	Formwork for F	
DAM3-C-B8-S-106	Pouring Concrete for Footings	1	13-May-26	13-May-26	16-Apr-26 A	16-Apr-26 A	127,306.23	127,306.23	127,306.23	100%	100%	Pouring Concr	
COLUMN NECK		17	14-May-26	04-Jun-26	14-Apr-26 A	12-May-26 A	120,554.54	120,554.54	120,554.54	100%	100%	12-May-26 A,	
DAM3-C-B8-S-257	Rebar for column neck	4	14-May-26	18-May-26	14-Apr-26 A	15-Apr-26 A	14,919.19	14,919.19	14,919.19	100%	100%	Rebar for colu	
DAM3-C-B8-S-267	Formwork for column neck	2	19-May-26	20-May-26	22-Apr-26 A	25-Apr-26 A	9,946.13	9,946.13	9,946.13	100%	100%	Formwork for c	
DAM3-C-B8-S-297	Pouring Concrete for column neck	1	21-May-26	21-May-26	23-Apr-26 A	25-Apr-26 A	24,865.31	24,865.31	24,865.31	100%	100%	Pouring Concr	
DAM3-C-B8-S-307	Damp proof /Bitumin paint on Footings & column neck	2	23-May-26	24-May-26	27-Apr-26 A	30-Apr-26 A	24,777.73	24,777.73	24,777.73	100%	100%	Damp proof /B	
DAM3-C-B8-S-367	Backfilling / Compaction up to Bottom of Grade Beams	7	25-May-26	04-Jun-26	05-May-26 A	12-May-26 A	46,046.19	46,046.19	46,046.19	100%	100%	Backfilling / C	
GRADE BEAM		24	20-Jun-26	09-Jul-26	13-May-26 A	03-Jun-26 A	171,632.86	171,632.86	171,632.86	100%	100%	03-Jun-26 A,	
DAM3-C-B8-S-338	Lean Concrete Below Grade Beams	2	23-Jun-26	24-Jun-26	13-May-26 A	13-May-26 A	4,431.19	4,431.19	4,431.19	100%	100%	Lean Concret	
DAM3-C-B8-S-337	Vapour barrier for Grade Beams	2	21-Jun-26	22-Jun-26	13-May-26 A	13-May-26 A	5,293.40	5,293.40	5,293.40	100%	100%	Vapour barrier	
DAM3-C-B8-S-527	Anti Termite Below Grade Beams	1	20-Jun-26	20-Jun-26	13-May-26 A	13-May-26 A	11,905.55	11,905.55	11,905.55	100%	100%	Anti Termite B	
DAM3-C-B8-S-339	Rebar for Grade Beams	5	25-Jun-26	30-Jun-26	16-May-26 A	20-May-26 A	27,194.46	27,194.46	27,194.46	100%	100%	Rebar for Gra	
DAM3-C-B8-S-341	Anchor bolts installation	2	01-Jul-26	02-Jul-26	17-May-26 A	20-May-26 A	57,238.83	57,238.83	57,238.83	100%	100%	Anchor bolts i	
DAM3-C-B8-S-340	Formwork for Grade Beams	2	01-Jul-26	02-Jul-26	20-May-26 A	23-May-26 A	6,798.61	6,798.61	6,798.61	100%	100%	Formwork for	
DAM3-C-B8-S-342	Pouring Concrete for Grade Beams	1	04-Jul-26	04-Jul-26	24-May-26 A	25-May-26 A	33,993.09	33,993.09	33,993.09	100%	100%	Pouring Conc	
DAM3-C-B8-S-347	Damp proof /Bitumin paint on Grade Beams	5	05-Jul-26	09-Jul-26	31-May-26 A	03-Jun-26 A	24,777.73	24,777.73	24,777.73	100%	100%	Damp proof /	
SLAB ON GRADE		25	11-Jul-26	17-Oct-26	04-Jun-26 A	19-Nov-26	397,232.98	396,325.87	396,325.87	99.77%	99.77%	19-Nov-	
DAM3-C-B8-S-377	Backfilling / Compaction for Slab on Grade	7	11-Jul-26	18-Jul-26	04-Jun-26 A	09-Jun-26 A	23,023.09	23,023.09	23,023.09	100%	100%	Backfilling / C	
DAM3-C-B8-S-382	Pouring Concrete for Ground Slab	4	22-Jul-26	26-Jul-26	13-Jul-26 A	16-Jul-26 A	344,195.21	344,195.21	344,195.21	100%	100%	Pouring Cor	
DAM3-C-B8-S-378	Anti Termite Treatment below Ground Slab	1	19-Jul-26	19-Jul-26	13-Jul-26 A	16-Jul-26 A	15,874.08	15,874.08	15,874.08	100%	100%	Anti Termite	
DAM3-C-B8-S-379	Vapour barrier for below Ground Slab	2	20-Jul-26	21-Jul-26	13-Jul-26 A	16-Jul-26 A	13,233.49	13,233.49	13,233.49	100%	100%	Vapour barr	
DAM3-C-B8-S-517	Concrete pad	7	10-Oct-26	17-Oct-26	12-Nov-26	19-Nov-26	907.11	0.00	0.00	0%	0%	Concret	
COLUMNS & BEAMS		34	27-Jul-26	29-Aug-26	16-May-26 A	03-Sep-26 A	101,966.98	101,966.98	101,966.98	100%	100%	03-Sep-26	
DAM3-C-B8-S-6103	Pouring Concrete for Tie Beams	1	19-Aug-26	20-Aug-26	16-May-26 A	25-May-26 A	9,079.54	9,079.54	9,079.54	100%	100%	Pouring Conc	
DAM3-C-B8-S-6101	Rebar for Tie Beams	4	09-Aug-26	12-Aug-26	16-May-26 A	23-May-26 A	7,263.64	7,263.64	7,263.64	100%	100%	Rebar for Tie	
DAM3-C-B8-S-6102	Formwork for Tie Beams	2	13-Aug-26	15-Aug-26	16-May-26 A	24-May-26 A	1,815.91	1,815.91	1,815.91	100%	100%	Formwork for	
DAM3-C-B8-S-5101	Rebar for column	5	27-Jul-26	01-Aug-26	02-Jul-26 A	11-Jul-26 A	20,144.05	20,144.05	20,144.05	100%	100%	Rebar for co	
DAM3-C-B8-S-5102	Formwork for column	4	02-Aug-26	05-Aug-26	07-Jul-26 A	25-Jul-26 A	5,036.01	5,036.01	5,036.01	100%	100%	Formwork fo	
DAM3-C-B8-S-5103	Pouring Concrete for column	1	08-Aug-26	08-Aug-26	13-Jul-26 A	26-Jul-26 A	25,180.06	25,180.06	25,180.06	100%	100%	Pouring Co	
DAM3-C-B8-S-6113	Rebar for Beams	4	20-Aug-26	25-Aug-26	23-Aug-26 A	26-Aug-26 A	13,379.11	13,379.11	13,379.11	100%	100%	Rebar for B	

Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary

Date	Revision	Checked	Approved
06-Oct-26	Weekly Report		

Activity ID	Activity Name	Original Duration	BL Project Start	BL Project Finish	Start	Finish	Budgeted Total Cost	Planned Value Cost	Earned Value Cost	Schedule % Complete	Performance % Complete
DAM3-C-B8-S-6123	Formwork for Beams	2	25-Aug-26	27-Aug-26	29-Aug-26 A	01-Sep-26 A	3,344.77	3,344.77	3,344.77	100%	100%
DAM3-C-B8-S-6133	Pouring Concrete for Beams	1	27-Aug-26	29-Aug-26	01-Sep-26 A	03-Sep-26 A	16,723.88	16,723.88	16,723.88	100%	100%
STRUCTURAL STEEL		44	05-Sep-26	14-Oct-26	14-Jun-26 A	07-Dec-26	1,566,668.48	1,218,745.08	1,539,773.29	77.79%	98.28%
DAM3-C-B8-SS-0100	Installation of columns	3	05-Sep-26	07-Sep-26	14-Jun-26 A	15-Jun-26 A	217,507.55	217,507.55	217,507.55	100%	100%
DAM3-C-B8-SS-0110	Installation of raft and purlins	5	08-Sep-26	13-Sep-26	15-Jun-26 A	16-Jun-26 A	326,261.32	326,261.32	326,261.32	100%	100%
DAM3-C-B8-SS-610	Intumescent paint to steel works	7	14-Sep-26	21-Sep-26	17-Jun-26 A	24-Jun-26 A	317,759.56	317,759.56	317,759.56	100%	100%
DAM3-C-B8-SS-0140	Installation of roof sheet	5	27-Sep-26	01-Oct-26	19-Jul-26 A	01-Aug-26 A	217,507.55	217,507.55	217,507.55	100%	100%
DAM3-C-B8-SS-0130	Installation of wall sandwich panel	5	10-Oct-26	14-Oct-26	02-Sep-26 A	22-Sep-26 A	326,261.32	0.00	326,261.32	0%	100%
DAM3-C-B8-SS-1030	Steel members for external platform	4	01-Oct-26	08-Oct-26	20-Sep-26 A	21-Sep-26 A	18,670.78	10,669.02	18,670.78	57.14%	100%
DAM3-C-B8-SS-620	Steel members for office area	4	22-Sep-26	30-Sep-26	26-Sep-26 A	28-Sep-26 A	115,805.20	115,805.20	115,805.20	100%	100%
DAM3-C-B8-SS-1020	Epoxy paint to steel members at office area	4	01-Oct-26	08-Oct-26	12-Nov-26	16-Nov-26	23,161.04	13,234.88	0.00	57.14%	0%
DAM3-C-B8-SS-1040	Epoxy paint for external platform	3	10-Oct-26	14-Oct-26	05-Dec-26	07-Dec-26	3,734.16	0.00	0.00	0%	0%
ARCHITECTURAL		93	14-Sep-26	13-Jan-27	18-Jul-26 A	28-Feb-27	900,244.66	61,869.68	209,103.78	6.87%	23.23%
MASONARY WORKS		18	14-Sep-26	17-Oct-26	23-Jul-26 A	23-Aug-26 A	78,954.21	61,869.68	78,954.21	78.36%	100%
DAM3-C-B8-A-0120	Block work at factory area	5	14-Sep-26	26-Sep-26	23-Jul-26 A	27-Jul-26 A	58,338.72	58,338.72	58,338.72	100%	100%
DAM3-C-B8-A-0150	Block work at office area	5	01-Oct-26	08-Oct-26	23-Jul-26 A	23-Aug-26 A	6,179.18	3,530.96	6,179.18	57.14%	100%
DAM3-C-B8-A-170	Block work at toilet area	3	10-Oct-26	17-Oct-26	27-Jul-26 A	22-Aug-26 A	14,436.31	0.00	14,436.31	0%	100%
WALL FINISHES		59	27-Oct-26	12-Dec-26	10-Sep-26 A	16-Jan-27	92,757.47	0.00	70,673.82	0%	76.19%
DAM3-C-B8-A-180	Internal Wall Plaster	10	27-Oct-26	12-Nov-26	10-Sep-26 A	28-Sep-26 A	48,590.16	0.00	48,590.16	0%	100%
DAM3-C-B8-A-230	Paint to Plaster (Primer, Putty & First Coat)	4	05-Dec-26	12-Dec-26	01-Oct-26 A	16-Jan-27	44,167.30	0.00	22,083.65	0%	50%
CIELING FINISHES		3	26-Nov-26	01-Dec-26	16-Jan-27	18-Jan-27	46,792.30	0.00	0.00	0%	0%
DAM3-C-B8-A-240	Installation of Ceiling Gypsum Board	3	26-Nov-26	01-Dec-26	16-Jan-27	18-Jan-27	46,792.30	0.00	0.00	0%	0%
FLOOR FINISHES		42	18-Nov-26	13-Jan-27	30-Sep-26 A	28-Feb-27	189,488.90	0.00	46,530.71	0%	24.56%
DAM3-C-B8-A-220	Tiles for Toilet	4	18-Nov-26	25-Nov-26	30-Sep-26 A	04-Oct-26 A	46,530.71	0.00	46,530.71	0%	100%
DAM3-C-B8-A-250	Tiles for Office Area	2	02-Dec-26	03-Dec-26	12-Jan-27	13-Jan-27	26,867.31	0.00	0.00	0%	0%
DAM3-C-B8-A-390	Granite strip	2	05-Dec-26	06-Dec-26	18-Jan-27	19-Jan-27	671.12	0.00	0.00	0%	0%
DAM3-C-B8-A-420	Epoxy paint	2	06-Jan-27	13-Jan-27	27-Feb-27	28-Feb-27	115,419.76	0.00	0.00	0%	0%
DOORS & WINDOWS		13	15-Oct-26	31-Oct-26	27-Sep-26 A	26-Nov-26	248,575.06	0.00	6,489.89	0%	2.61%
DAM3-C-B8-A-558	Skylight fixtures installation	1	31-Oct-26	31-Oct-26	27-Sep-26 A	30-Sep-26 A	6,489.89	0.00	6,489.89	0%	100%
DAM3-C-B8-A-552	Window (CW1)	7	15-Oct-26	22-Oct-26	12-Nov-26	19-Nov-26	94,173.21	0.00	0.00	0%	0%
DAM3-C-B8-A-553	Roll up Shutter Door	1	24-Oct-26	24-Oct-26	21-Nov-26	21-Nov-26	68,619.20	0.00	0.00	0%	0%
DAM3-C-B8-A-200	Supply and install (D5) 1000*2200mm single leaf steel door with door	1	25-Oct-26	25-Oct-26	22-Nov-26	22-Nov-26	16,016.16	0.00	0.00	0%	0%
DAM3-C-B8-A-554	Supply and install (D4) 800*2200 mm single leaf aluminum door with door	1	26-Oct-26	26-Oct-26	23-Nov-26	23-Nov-26	22,737.85	0.00	0.00	0%	0%
DAM3-C-B8-A-555	Supply and install (D7) 1000*2200 mm single leaf aluminum door with door	1	27-Oct-26	27-Oct-26	24-Nov-26	24-Nov-26	7,811.07	0.00	0.00	0%	0%
DAM3-C-B8-A-556	Supply and install (D3) 1000*2200 mm single leaf aluminum door with door	1	28-Oct-26	28-Oct-26	25-Nov-26	25-Nov-26	16,016.16	0.00	0.00	0%	0%
DAM3-C-B8-A-557	Supply and install fire rated 45 min (D2) 1200*2200 mm single leaf steel doo	1	29-Oct-26	29-Oct-26	26-Nov-26	26-Nov-26	16,711.52	0.00	0.00	0%	0%
WATER PROOFING WORKS		4	14-Nov-26	17-Nov-26	28-Nov-26	01-Dec-26	4,879.02	0.00	0.00	0%	0%
DAM3-C-B8-A-370	Waterproofing membrane for toilets	4	14-Nov-26	17-Nov-26	28-Nov-26	01-Dec-26	4,879.02	0.00	0.00	0%	0%
METAL WORKS		23	07-Dec-26	21-Dec-26	18-Jul-26 A	09-Feb-27	193,717.06	0.00	6,455.16	0%	3.33%
DAM3-C-B8-A-300	Galvanised Steel Gratings	2	20-Dec-26	21-Dec-26	18-Jul-26 A	18-Jul-26 A	6,455.16	0.00	6,455.16	0%	100%
DAM3-C-B8-A-290	Steel Ladder	2	07-Dec-26	08-Dec-26	20-Jan-27	21-Jan-27	9,839.16	0.00	0.00	0%	0%
DAM3-C-B8-A-291	Steel railing works	4	09-Dec-26	13-Dec-26	23-Jan-27	26-Jan-27	1,533.98	0.00	0.00	0%	0%
DAM3-C-B8-A-292	Aluminium composite panel	3	14-Dec-26	19-Dec-26	07-Feb-27	09-Feb-27	175,888.76	0.00	0.00	0%	0%
SPECIALTIES		7	27-Dec-26	05-Jan-27	17-Feb-27	25-Feb-27	45,080.66	0.00	0.00	0%	0%
DAM3-C-B8-A-320	Installation of fittings	3	27-Dec-26	31-Dec-26	17-Feb-27	20-Feb-27	22,981.27	0.00	0.00	0%	0%
DAM3-C-B8-A-570	Identification sign; ID01 & ID02	3	02-Jan-27	04-Jan-27	21-Feb-27	24-Feb-27	9,630.56	0.00	0.00	0%	0%
DAM3-C-B8-A-340	Furniture Installation	1	05-Jan-27	05-Jan-27	25-Feb-27	25-Feb-27	12,468.83	0.00	0.00	0%	0%
MECHANICAL		108	11-Jul-26	05-Jan-27	15-Jun-26 A	20-Feb-27	467,522.66	18,585.14	156,280.78	3.98%	33.43%
HVAC		14	13-Dec-26	28-Dec-26	17-Jan-27	01-Feb-27	233,183.33	0.00	0.00	0%	0%

Activity ID	Activity Name	Original Duration	BL Project Start	BL Project Finish	Start	Finish	Budgeted Total Cost	Planned Value Cost	Earned Value Cost	Schedule % Complete	Performance % Complete
FIRST STAGE		4	20-Dec-26	23-Dec-26	24-Jan-27	27-Jan-27	170,694.73	0.00	0.00	0%	0%
DAM3-C-B8-M-140	Installation of HVAC Ducts	2	20-Dec-26	21-Dec-26	24-Jan-27	25-Jan-27	149,489.33	0.00	0.00	0%	0%
DAM3-C-B8-M-170	Installation of Duct insulation	2	22-Dec-26	23-Dec-26	26-Jan-27	27-Jan-27	21,205.40	0.00	0.00	0%	0%
SECOND STAGE		14	13-Dec-26	28-Dec-26	17-Jan-27	01-Feb-27	62,488.60	0.00	0.00	0%	0%
DAM3-C-B8-M-130	Installation of Exhaust Fans	2	13-Dec-26	14-Dec-26	17-Jan-27	18-Jan-27	7,938.56	0.00	0.00	0%	0%
DAM3-C-B8-M-160	Installation of Wall Propeller Type Exhaust Fan	4	15-Dec-26	19-Dec-26	19-Jan-27	23-Jan-27	46,831.64	0.00	0.00	0%	0%
DAM3-C-B8-M-339	Installation of Diffuser	2	24-Dec-26	26-Dec-26	28-Jan-27	30-Jan-27	2,144.00	0.00	0.00	0%	0%
DAM3-C-B8-M-340	Supply, install, test and commission door grilles & exhaust louvers	2	27-Dec-26	28-Dec-26	31-Jan-27	01-Feb-27	5,574.40	0.00	0.00	0%	0%
FIRE FIGHTING SYSTEM		17	13-Dec-26	05-Jan-27	12-Aug-26 A	20-Feb-27	102,458.78	0.00	84,594.16	0%	82.56%
FIRST STAGE		11	13-Dec-26	26-Dec-26	12-Aug-26 A	16-Aug-26 A	84,594.16	0.00	84,594.16	0%	100%
DAM3-C-B8-M-300	Installation of Fire Fighting Pipes (Seamless Black Steel)	4	13-Dec-26	20-Dec-26	12-Aug-26 A	16-Aug-26 A	72,394.75	0.00	72,394.75	0%	100%
DAM3-C-B8-M-310	Installation of Fire Fighting Valve	5	21-Dec-26	26-Dec-26	15-Aug-26 A	16-Aug-26 A	12,199.40	0.00	12,199.40	0%	100%
SECOND STAGE		16	29-Dec-26	05-Jan-27	02-Feb-27	20-Feb-27	17,864.62	0.00	0.00	0%	0%
DAM3-C-B8-M-370	Supply, install, test and commission Fire Department Connection(FDC)	3	29-Dec-26	31-Dec-26	02-Feb-27	04-Feb-27	2,706.06	0.00	0.00	0%	0%
DAM3-C-B8-M-320	Installation of Fire Hose Cabinet	3	03-Jan-27	05-Jan-27	17-Feb-27	20-Feb-27	15,158.56	0.00	0.00	0%	0%
SEWER AND DRAINAGE SYSTEM		91	11-Jul-26	20-Dec-26	15-Jun-26 A	30-Jan-27	90,009.74	18,585.14	30,093.94	20.65%	33.43%
FIRST STAGE		91	11-Jul-26	03-Dec-26	15-Jun-26 A	13-Jan-27	41,149.90	18,585.14	30,093.94	45.16%	73.13%
DAM3-C-B8-M-200	Installation of Sanitary Waste / Drainage Pipes	4	11-Jul-26	14-Jul-26	15-Jun-26 A	20-Jun-26 A	18,585.14	18,585.14	18,585.14	100%	100%
DAM3-C-B8-M-380	Installation of Trench drain	5	29-Nov-26	03-Dec-26	20-Jun-26 A	21-Jun-26 A	11,508.80	0.00	11,508.80	0%	100%
DAM3-C-B8-M-220	Installation of Floor Drain	2	26-Nov-26	28-Nov-26	12-Jan-27	13-Jan-27	11,055.96	0.00	0.00	0%	0%
SECOND STAGE		14	05-Dec-26	20-Dec-26	14-Jan-27	30-Jan-27	48,859.84	0.00	0.00	0%	0%
DAM3-C-B8-M-180	Installation of Electric Water Heater	2	05-Dec-26	06-Dec-26	14-Jan-27	16-Jan-27	1,819.51	0.00	0.00	0%	0%
DAM3-C-B8-M-190	Installation of Sanitary Fixture and Accessories	4	07-Dec-26	10-Dec-26	17-Jan-27	20-Jan-27	19,921.72	0.00	0.00	0%	0%
DAM3-C-B8-M-210	Installation of Lavotary /Wash Basin	2	12-Dec-26	13-Dec-26	21-Jan-27	23-Jan-27	21,416.68	0.00	0.00	0%	0%
DAM3-C-B8-M-270	Installation of Bib Tap	2	14-Dec-26	15-Dec-26	24-Jan-27	25-Jan-27	1,900.66	0.00	0.00	0%	0%
DAM3-C-B8-M-428	Installation of Water Tap	2	16-Dec-26	17-Dec-26	26-Jan-27	27-Jan-27	2,874.14	0.00	0.00	0%	0%
DAM3-C-B8-M-429	Installation of Roof Vent Cap	2	19-Dec-26	20-Dec-26	28-Jan-27	30-Jan-27	927.12	0.00	0.00	0%	0%
WATER SUPPLY SYSTEM		15	13-Dec-26	24-Dec-26	05-Sep-26 A	19-Jan-27	41,870.81	0.00	41,592.68	0%	99.34%
FIRST STAGE		8	13-Dec-26	19-Dec-26	05-Sep-26 A	09-Sep-26 A	41,592.68	0.00	41,592.68	0%	100%
DAM3-C-B8-M-290	Installation of Water Supply Pipes	4	13-Dec-26	16-Dec-26	05-Sep-26 A	08-Sep-26 A	23,318.41	0.00	23,318.41	0%	100%
DAM3-C-B8-M-280	Installation of Water Supply Valve	2	17-Dec-26	19-Dec-26	06-Sep-26 A	09-Sep-26 A	18,274.27	0.00	18,274.27	0%	100%
SECOND STAGE		3	20-Dec-26	24-Dec-26	17-Jan-27	19-Jan-27	278.13	0.00	0.00	0%	0%
DAM3-C-B8-M-330	Capped connection	3	20-Dec-26	24-Dec-26	17-Jan-27	19-Jan-27	278.13	0.00	0.00	0%	0%
ELECTRICAL		61	18-Oct-26	14-Jan-27	19-May-26 A	03-Feb-27	752,044.76	0.00	27,642.87	0%	3.68%
FIRST STAGE		61	18-Oct-26	29-Nov-26	19-May-26 A	05-Jan-27	86,114.12	0.00	27,642.87	0%	32.1%
DAM3-C-B8-E-113	Installation of Earthing and Grounding	3	24-Nov-26	29-Nov-26	19-May-26 A	05-Jan-27	19,646.47	0.00	17,681.82	0%	90%
DAM3-C-B8-E-143	Installation of Conduits and wiring outlets - Fire Alarm System	4	18-Oct-26	21-Oct-26	20-May-26 A	09-Dec-26	1,768.31	0.00	884.15	0%	50%
DAM3-C-B8-E-183	Installation of Sleeves & Power outlet	8	18-Oct-26	26-Oct-26	20-May-26 A	22-Nov-26	2,920.45	0.00	1,460.23	0%	50%
DAM3-C-B8-E-163	Installation of Conduites for Lighting Fixture	4	01-Nov-26	04-Nov-26	07-Sep-26 A	20-Dec-26	8,462.97	0.00	7,616.67	0%	90%
DAM3-C-B8-E-233	Installation of Wires	4	05-Nov-26	09-Nov-26	20-Dec-26	24-Dec-26	16,925.94	0.00	0.00	0%	0%
DAM3-C-B8-E-223	Installation of LV Cables	2	19-Nov-26	23-Nov-26	03-Jan-27	05-Jan-27	36,389.98	0.00	0.00	0%	0%
SECOND STAGE		48	22-Oct-26	14-Jan-27	10-Dec-26	03-Feb-27	665,930.64	0.00	0.00	0%	0%
DAM3-C-B8-E-123	Installation of Fire Alarm Control Panel	4	22-Oct-26	26-Oct-26	10-Dec-26	14-Dec-26	19,451.37	0.00	0.00	0%	0%
DAM3-C-B8-E-133	Installation of Fire Detectors & Accessories	4	27-Oct-26	31-Oct-26	15-Dec-26	19-Dec-26	56,740.37	0.00	0.00	0%	0%
DAM3-C-B8-E-153	Installation of Lighting fixtures	4	10-Nov-26	14-Nov-26	24-Dec-26	29-Dec-26	76,166.74	0.00	0.00	0%	0%
DAM3-C-B8-E-193	Installation of Main Distribution Board	2	10-Nov-26	11-Nov-26	24-Dec-26	27-Dec-26	32,472.73	0.00	0.00	0%	0%
DAM3-C-B8-E-410	Installation of CCTV System	3	10-Nov-26	17-Nov-26	24-Dec-26	28-Dec-26	76,349.24	0.00	0.00	0%	0%
DAM3-C-B8-E-243	Installation of LP-1 Panel	2	12-Nov-26	14-Nov-26	27-Dec-26	29-Dec-26	18,403.54	0.00	0.00	0%	0%
DAM3-C-B8-E-273	Installation of Access Control System	3	18-Nov-26	23-Nov-26	28-Dec-26	31-Dec-26	27,616.86	0.00	0.00	0%	0%

Activity ID	Activity Name	Original Duration	BL Project Start	BL Project Finish	Start	Finish	Budgeted Total Cost	Planned Value Cost	Earned Value Cost	Schedule % Complete	Performance % Complete
DAM3-C-B8-E-253	Installation of PP-AC panel	2	15-Nov-26	16-Nov-26	29-Dec-26	31-Dec-26	21,648.48	0.00	0.00	0%	0%
DAM3-C-B8-E-213	Installation of Telephone Cabinet	2	17-Nov-26	18-Nov-26	31-Dec-26	03-Jan-27	26,991.08	0.00	0.00	0%	0%
DAM3-C-B8-E-283	Monitor Modules for Fire Alarm	2	24-Nov-26	25-Nov-26	31-Dec-26	03-Jan-27	3,882.38	0.00	0.00	0%	0%
DAM3-C-B8-E-293	Line Isolator Modules for Fire Alarm	2	26-Nov-26	28-Nov-26	03-Jan-27	05-Jan-27	185.40	0.00	0.00	0%	0%
DAM3-C-B8-E-303	Firewarning flash light with sounder; wall mounted, Weather proof	2	29-Nov-26	30-Nov-26	05-Jan-27	07-Jan-27	3,082.69	0.00	0.00	0%	0%
DAM3-C-B8-E-173	Installation of Wiring Devices	3	13-Dec-26	16-Dec-26	17-Jan-27	19-Jan-27	19,435.09	0.00	0.00	0%	0%
DAM3-C-B8-E-203	Installation of Disconnect Switches	2	17-Dec-26	19-Dec-26	20-Jan-27	21-Jan-27	30,235.95	0.00	0.00	0%	0%
DAM3-C-B8-E-420	Installation of Solar power plant	7	07-Jan-27	14-Jan-27	26-Jan-27	03-Feb-27	253,268.71	0.00	0.00	0%	0%
BLOCK B9		287	25-Feb-26	31-Jan-27	17-Feb-26 A	13-Feb-27	5,075,523.09	2,666,759.17	3,339,986.43	52.54%	65.81%
STRUCTURAL		210	25-Feb-26	20-Oct-26	17-Feb-26 A	19-Nov-26	1,389,042.53	1,388,135.41	1,388,135.41	99.93%	99.93%
FOOTING		96	25-Feb-26	13-May-26	17-Feb-26 A	23-Apr-26 A	597,655.16	597,655.16	597,655.16	100%	100%
DAM3-C-B9-S-150	Excavation for footings	4	25-Feb-26	02-Mar-26	17-Feb-26 A	21-Feb-26 A	89,859.61	89,859.61	89,859.61	100%	100%
DAM3-C-B9-S-6303	Soil replacement - rock fill	4	03-Mar-26	07-Mar-26	03-Mar-26 A	07-Mar-26 A	179,061.91	179,061.91	179,061.91	100%	100%
DAM3-C-B9-S-6313	Engineering fill	4	08-Mar-26	11-Mar-26	09-Mar-26 A	17-Mar-26 A	46,046.19	46,046.19	46,046.19	100%	100%
DAM3-C-B9-S-102	Vapour Barrier for Footings	1	14-Mar-26	14-Mar-26	29-Mar-26 A	29-Mar-26 A	7,940.10	7,940.10	7,940.10	100%	100%
DAM3-C-B9-S-101	Anti Termite Below Footings	1	12-Mar-26	12-Mar-26	29-Mar-26 A	29-Mar-26 A	11,905.55	11,905.55	11,905.55	100%	100%
DAM3-C-B9-S-103	Lean Concrete Below Footings	2	15-Mar-26	16-Mar-26	30-Mar-26 A	30-Mar-26 A	8,229.34	8,229.34	8,229.34	100%	100%
DAM3-C-B9-S-104	Rebar for Footings	4	04-May-26	07-May-26	18-Apr-26 A	20-Apr-26 A	101,844.98	101,844.98	101,844.98	100%	100%
DAM3-C-B9-S-105	Formwork for Footings	4	09-May-26	12-May-26	19-Apr-26 A	21-Apr-26 A	25,461.25	25,461.25	25,461.25	100%	100%
DAM3-C-B9-S-106	Pouring Concrete for Footings	1	13-May-26	13-May-26	23-Apr-26 A	23-Apr-26 A	127,306.23	127,306.23	127,306.23	100%	100%
COLUMN NECK		14	14-May-26	04-Jun-26	21-Apr-26 A	14-May-26 A	120,554.54	120,554.54	120,554.54	100%	100%
DAM3-C-B9-S-257	Rebar for column neck	4	14-May-26	18-May-26	21-Apr-26 A	22-Apr-26 A	14,919.19	14,919.19	14,919.19	100%	100%
DAM3-C-B9-S-267	Formwork for column neck	2	19-May-26	20-May-26	22-Apr-26 A	23-Apr-26 A	9,946.13	9,946.13	9,946.13	100%	100%
DAM3-C-B9-S-297	Pouring Concrete for column neck	1	21-May-26	21-May-26	28-Apr-26 A	28-Apr-26 A	24,865.31	24,865.31	24,865.31	100%	100%
DAM3-C-B9-S-307	Damp proof /Bitumin paint on Footings & column neck	2	23-May-26	24-May-26	02-May-26 A	02-May-26 A	24,777.73	24,777.73	24,777.73	100%	100%
DAM3-C-B9-S-367	Backfilling / Compaction up to Bottom of Grade Beams	7	25-May-26	04-Jun-26	09-May-26 A	14-May-26 A	46,046.19	46,046.19	46,046.19	100%	100%
GRADE BEAM		41	06-Jun-26	01-Jul-26	18-May-26 A	07-Jun-26 A	171,632.86	171,632.86	171,632.86	100%	100%
DAM3-C-B9-S-338	Lean Concrete Below Grade Beams	2	09-Jun-26	10-Jun-26	18-May-26 A	18-May-26 A	4,431.19	4,431.19	4,431.19	100%	100%
DAM3-C-B9-S-337	Vapour barrier for Grade Beams	2	07-Jun-26	08-Jun-26	18-May-26 A	18-May-26 A	5,293.40	5,293.40	5,293.40	100%	100%
DAM3-C-B9-S-527	Anti Termite Below Grade Beams	1	06-Jun-26	06-Jun-26	18-May-26 A	18-May-26 A	11,905.55	11,905.55	11,905.55	100%	100%
DAM3-C-B9-S-339	Rebar for Grade Beams	5	17-Jun-26	22-Jun-26	20-May-26 A	21-May-26 A	27,194.46	27,194.46	27,194.46	100%	100%
DAM3-C-B9-S-341	Anchor bolts installation	2	23-Jun-26	24-Jun-26	20-May-26 A	23-May-26 A	57,238.83	57,238.83	57,238.83	100%	100%
DAM3-C-B9-S-340	Formwork for Grade Beams	2	23-Jun-26	24-Jun-26	21-May-26 A	24-May-26 A	6,798.61	6,798.61	6,798.61	100%	100%
DAM3-C-B9-S-342	Pouring Concrete for Grade Beams	1	25-Jun-26	25-Jun-26	25-May-26 A	25-May-26 A	33,993.09	33,993.09	33,993.09	100%	100%
DAM3-C-B9-S-347	Damp proof /Bitumin paint on Grade Beams	5	27-Jun-26	01-Jul-26	02-Jun-26 A	07-Jun-26 A	24,777.73	24,777.73	24,777.73	100%	100%
SLAB ON GRADE		81	15-Jul-26	20-Oct-26	09-Jun-26 A	19-Nov-26	397,232.98	396,325.87	396,325.87	99.77%	99.77%
DAM3-C-B9-S-377	Backfilling / Compaction for Slab on Grade	7	15-Jul-26	22-Jul-26	09-Jun-26 A	13-Jun-26 A	23,023.09	23,023.09	23,023.09	100%	100%
DAM3-C-B9-S-382	Pouring Concrete for Ground Slab	4	27-Jul-26	30-Jul-26	22-Jul-26 A	25-Jul-26 A	344,195.21	344,195.21	344,195.21	100%	100%
DAM3-C-B9-S-378	Anti Termite Treatment below Ground Slab	1	23-Jul-26	23-Jul-26	22-Jul-26 A	25-Jul-26 A	15,874.08	15,874.08	15,874.08	100%	100%
DAM3-C-B9-S-379	Vapour barrier for below Ground Slab	2	25-Jul-26	26-Jul-26	22-Jul-26 A	25-Jul-26 A	13,233.49	13,233.49	13,233.49	100%	100%
DAM3-C-B9-S-517	Concrete pad	7	13-Oct-26	20-Oct-26	12-Nov-26	19-Nov-26	907.11	0.00	0.00	0%	0%
COLUMNS & BEAMS		74	23-Jul-26	19-Aug-26	21-May-26 A	12-Sep-26 A	101,966.98	101,966.98	101,966.98	100%	100%
DAM3-C-B9-S-6101	Rebar for Tie Beams	4	04-Aug-26	08-Aug-26	21-May-26 A	07-Jun-26 A	7,263.64	7,263.64	7,263.64	100%	100%
DAM3-C-B9-S-6102	Formwork for Tie Beams	2	09-Aug-26	10-Aug-26	23-May-26 A	08-Jun-26 A	1,815.91	1,815.91	1,815.91	100%	100%
DAM3-C-B9-S-6103	Pouring Concrete for Tie Beams	1	11-Aug-26	11-Aug-26	25-May-26 A	09-Jun-26 A	9,079.54	9,079.54	9,079.54	100%	100%
DAM3-C-B9-S-5101	Rebar for column	5	23-Jul-26	28-Jul-26	11-Jul-26 A	14-Jul-26 A	20,144.05	20,144.05	20,144.05	100%	100%
DAM3-C-B9-S-5102	Formwork for column	4	29-Jul-26	02-Aug-26	14-Jul-26 A	28-Jul-26 A	5,036.01	5,036.01	5,036.01	100%	100%
DAM3-C-B9-S-5103	Pouring Concrete for column	1	03-Aug-26	03-Aug-26	15-Jul-26 A	29-Jul-26 A	25,180.06	25,180.06	25,180.06	100%	100%
DAM3-C-B9-S-6113	Rebar for Beams	4	12-Aug-26	16-Aug-26	23-Aug-26 A	26-Aug-26 A	13,379.11	13,379.11	13,379.11	100%	100%

Date	Revision	Checked	Approved
06-Oct-26	Weekly Report		

Activity ID	Activity Name	Original Duration	BL Project Start	BL Project Finish	Start	Finish	Budgeted Total Cost	Planned Value Cost	Earned Value Cost	Schedule % Complete	Performance % Complete
DAM3-C-B9-S-6123	Formwork for Beams	2	17-Aug-26	18-Aug-26	01-Sep-26 A	05-Sep-26 A	3,344.77	3,344.77	3,344.77	100%	100%
DAM3-C-B9-S-6133	Pouring Concrete for Beams	1	19-Aug-26	19-Aug-26	08-Sep-26 A	12-Sep-26 A	16,723.88	16,723.88	16,723.88	100%	100%
STRUCTURAL STEEL		48	08-Sep-26	18-Oct-26	16-Jun-26 A	19-Nov-26	1,566,668.48	1,200,817.16	1,539,773.29	76.65%	98.28%
DAM3-C-B9-SS-0100	Installation of columns	3	08-Sep-26	10-Sep-26	16-Jun-26 A	17-Jun-26 A	217,507.55	217,507.55	217,507.55	100%	100%
DAM3-C-B9-SS-0110	Installation of raft and purlins	5	12-Sep-26	16-Sep-26	18-Jun-26 A	22-Jun-26 A	326,261.32	326,261.32	326,261.32	100%	100%
DAM3-C-B9-SS-610	Intumescent paint to steel works	7	17-Sep-26	26-Sep-26	05-Jul-26 A	07-Jul-26 A	317,759.56	317,759.56	317,759.56	100%	100%
DAM3-C-B9-SS-0140	Installation of roof sheet	5	30-Sep-26	05-Oct-26	22-Jul-26 A	01-Aug-26 A	217,507.55	217,507.55	217,507.55	100%	100%
DAM3-C-B9-SS-0130	Installation of wall sandwich panel	5	13-Oct-26	18-Oct-26	03-Sep-26 A	05-Oct-26 A	326,261.32	0.00	326,261.32	0%	100%
DAM3-C-B9-SS-1030	Steel members for external platform	7	05-Oct-26	12-Oct-26	21-Sep-26 A	26-Sep-26 A	18,670.78	2,667.25	18,670.78	14.29%	100%
DAM3-C-B9-SS-620	Steel members for office area	2	27-Sep-26	04-Oct-26	27-Sep-26 A	29-Sep-26 A	115,805.20	115,805.20	115,805.20	100%	100%
DAM3-C-B9-SS-1020	Epoxy paint to steel members at office area	7	05-Oct-26	12-Oct-26	12-Nov-26	19-Nov-26	23,161.04	3,308.72	0.00	14.29%	0%
DAM3-C-B9-SS-1040	Epoxy paint for external platform	5	13-Oct-26	18-Oct-26	12-Nov-26	17-Nov-26	3,734.16	0.00	0.00	0%	0%
ARCHITECTURAL		83	17-Sep-26	12-Jan-27	27-Jul-26 A	03-Feb-27	900,244.66	59,221.46	228,154.08	6.58%	25.34%
MASONARY WORKS		19	17-Sep-26	20-Oct-26	28-Jul-26 A	29-Aug-26 A	78,954.21	59,221.46	78,954.21	75.01%	100%
DAM3-C-B9-A-0120	Block work at factory area	10	17-Sep-26	29-Sep-26	28-Jul-26 A	30-Jul-26 A	58,338.72	58,338.72	58,338.72	100%	100%
DAM3-C-B9-A-0150	Block work at office area	5	05-Oct-26	12-Oct-26	30-Jul-26 A	27-Aug-26 A	6,179.18	882.74	6,179.18	14.29%	100%
DAM3-C-B9-A-170	Block work at toilet area	5	13-Oct-26	20-Oct-26	02-Aug-26 A	29-Aug-26 A	14,436.31	0.00	14,436.31	0%	100%
WALL FINISHES		26	31-Oct-26	15-Dec-26	17-Sep-26 A	13-Dec-26	92,757.47	0.00	48,590.16	0%	52.38%
DAM3-C-B9-A-180	Internal Wall Plaster	5	31-Oct-26	16-Nov-26	17-Sep-26 A	05-Oct-26 A	48,590.16	0.00	48,590.16	0%	100%
DAM3-C-B9-A-230	Paint to Plaster (Primer, Putty & First Coat)	4	08-Dec-26	15-Dec-26	09-Dec-26	13-Dec-26	44,167.30	0.00	0.00	0%	0%
CIELING FINISHES		3	30-Nov-26	05-Dec-26	03-Dec-26	06-Dec-26	46,792.30	0.00	0.00	0%	0%
DAM3-C-B9-A-240	Installation of Ceiling Gypsum Board	3	30-Nov-26	05-Dec-26	03-Dec-26	06-Dec-26	46,792.30	0.00	0.00	0%	0%
FLOOR FINISHES		56	22-Nov-26	12-Jan-27	01-Oct-26 A	03-Feb-27	189,488.90	0.00	34,898.03	0%	18.42%
DAM3-C-B9-A-220	Tiles for Toilet	4	22-Nov-26	29-Nov-26	01-Oct-26 A	02-Dec-26	46,530.71	0.00	34,898.03	0%	75%
DAM3-C-B9-A-250	Tiles for Office Area	2	06-Dec-26	07-Dec-26	07-Dec-26	08-Dec-26	26,867.31	0.00	0.00	0%	0%
DAM3-C-B9-A-390	Granite strip	2	08-Dec-26	09-Dec-26	09-Dec-26	10-Dec-26	671.12	0.00	0.00	0%	0%
DAM3-C-B9-A-420	Epoxy paint	4	05-Jan-27	12-Jan-27	31-Jan-27	03-Feb-27	115,419.76	0.00	0.00	0%	0%
DOORS & WINDOWS		13	19-Oct-26	03-Nov-26	30-Sep-26 A	26-Nov-26	248,575.06	0.00	6,489.89	0%	2.61%
DAM3-C-B9-A-558	Skylight fixtures installation	1	03-Nov-26	03-Nov-26	30-Sep-26 A	04-Oct-26 A	6,489.89	0.00	6,489.89	0%	100%
DAM3-C-B9-A-552	Window (CW1)	7	19-Oct-26	26-Oct-26	12-Nov-26	19-Nov-26	94,173.21	0.00	0.00	0%	0%
DAM3-C-B9-A-553	Roll up Shutter Door	1	27-Oct-26	27-Oct-26	21-Nov-26	21-Nov-26	68,619.20	0.00	0.00	0%	0%
DAM3-C-B9-A-200	Supply and install (D5) 1000*2200mm single leaf steel door with door	1	28-Oct-26	28-Oct-26	22-Nov-26	22-Nov-26	16,016.16	0.00	0.00	0%	0%
DAM3-C-B9-A-554	Supply and install (D4) 800*2200 mm single leaf aluminum door with door	1	29-Oct-26	29-Oct-26	23-Nov-26	23-Nov-26	22,737.85	0.00	0.00	0%	0%
DAM3-C-B9-A-555	Supply and install (D7) 1000*2200 mm single leaf aluminum door with door	1	31-Oct-26	31-Oct-26	24-Nov-26	24-Nov-26	7,811.07	0.00	0.00	0%	0%
DAM3-C-B9-A-556	Supply and install (D3) 1000*2200 mm single leaf aluminum door with door	1	01-Nov-26	01-Nov-26	25-Nov-26	25-Nov-26	16,016.16	0.00	0.00	0%	0%
DAM3-C-B9-A-557	Supply and install fire rated 45 min (D2) 1200*2200 mm single leaf steel doo	1	02-Nov-26	02-Nov-26	26-Nov-26	26-Nov-26	16,711.52	0.00	0.00	0%	0%
WATER PROOFING WORKS		4	17-Nov-26	21-Nov-26	28-Nov-26	01-Dec-26	4,879.02	0.00	0.00	0%	0%
DAM3-C-B9-A-370	Waterproofing membrane for toilets	4	17-Nov-26	21-Nov-26	28-Nov-26	01-Dec-26	4,879.02	0.00	0.00	0%	0%
METAL WORKS		58	10-Dec-26	24-Dec-26	27-Jul-26 A	20-Dec-26	193,717.06	0.00	59,221.79	0%	30.57%
DAM3-C-B9-A-300	Galvanised Steel Gratings	2	23-Dec-26	24-Dec-26	27-Jul-26 A	27-Jul-26 A	6,455.16	0.00	6,455.16	0%	100%
DAM3-C-B9-A-292	Aluminium composite panel	3	17-Dec-26	22-Dec-26	29-Sep-26 A	20-Dec-26	175,888.76	0.00	52,766.63	0%	30%
DAM3-C-B9-A-290	Steel Ladder	2	10-Dec-26	12-Dec-26	12-Dec-26	13-Dec-26	9,839.16	0.00	0.00	0%	0%
DAM3-C-B9-A-291	Steel railing works	3	13-Dec-26	16-Dec-26	14-Dec-26	16-Dec-26	1,533.98	0.00	0.00	0%	0%
SPECIALTIES		7	26-Dec-26	04-Jan-27	23-Jan-27	30-Jan-27	45,080.66	0.00	0.00	0%	0%
DAM3-C-B9-A-320	Installation of fittings	3	26-Dec-26	30-Dec-26	23-Jan-27	25-Jan-27	22,981.27	0.00	0.00	0%	0%
DAM3-C-B9-A-570	Identification sign; ID01 & ID02	3	31-Dec-26	03-Jan-27	26-Jan-27	28-Jan-27	9,630.56	0.00	0.00	0%	0%
DAM3-C-B9-A-340	Furniture Installation	1	04-Jan-27	04-Jan-27	30-Jan-27	30-Jan-27	12,468.83	0.00	0.00	0%	0%
MECHANICAL		158	02-Jul-26	04-Jan-27	21-Jun-26 A	02-Jan-27	467,522.66	18,585.14	156,280.78	3.98%	33.43%
HVAC		14	16-Dec-26	31-Dec-26	14-Dec-26	29-Dec-26	233,183.33	0.00	0.00	0%	0%

2026 2027

Formwork
Pouring C
19-Nov-
Installation o
Installation o
Intumescent
Installation
Installatio
Steel mer
Steel mer
Epoxy p
Epoxy p
03-Fe
29-Aug-26
Block work
Block work
Block work
13-Dec
Internal W
Paint to
06-Dec
Installa
03-Fe
Tiles for
Tiles fo
Granite
Epoxy
26-Nov-
Skylight f
Window
Roll up
Supply
Supply
Supply
Supply
Supply
01-Dec
Waterp
20-Dec
Galvanised
Alumin
Steel L
Steel ra
30-Ja
Install
Identif
Furnit
02-Jar
29-Dec

Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary

Date	Revision	Checked	Approved
06-Oct-26	Weekly Report		

Activity ID	Activity Name	Original Duration	BL Project Start	BL Project Finish	Start	Finish	Budgeted Total Cost	Planned Value Cost	Earned Value Cost	Schedule % Complete	Performance % Complete
FIRST STAGE		4	23-Dec-26	27-Dec-26	21-Dec-26	24-Dec-26	170,694.73	0.00	0.00	0%	0%
DAM3-C-B9-M-140	Installation of HVAC Ducts	2	23-Dec-26	24-Dec-26	21-Dec-26	22-Dec-26	149,489.33	0.00	0.00	0%	0%
DAM3-C-B9-M-170	Installation of Duct insulation	2	26-Dec-26	27-Dec-26	23-Dec-26	24-Dec-26	21,205.40	0.00	0.00	0%	0%
SECOND STAGE		14	16-Dec-26	31-Dec-26	14-Dec-26	29-Dec-26	62,488.60	0.00	0.00	0%	0%
DAM3-C-B9-M-130	Installation of Exhaust Fans	2	16-Dec-26	17-Dec-26	14-Dec-26	15-Dec-26	7,938.56	0.00	0.00	0%	0%
DAM3-C-B9-M-160	Installation of Wall Propeller Type Exhaust Fan	4	19-Dec-26	22-Dec-26	16-Dec-26	20-Dec-26	46,831.64	0.00	0.00	0%	0%
DAM3-C-B9-M-339	Installation of Diffuser	2	28-Dec-26	29-Dec-26	26-Dec-26	27-Dec-26	2,144.00	0.00	0.00	0%	0%
DAM3-C-B9-M-340	Supply, install, test and commission door grilles & exhaust louvers	2	30-Dec-26	31-Dec-26	28-Dec-26	29-Dec-26	5,574.40	0.00	0.00	0%	0%
FIRE FIGHTING SYSTEM		20	16-Dec-26	04-Jan-27	17-Aug-26 A	02-Jan-27	102,458.78	0.00	84,594.16	0%	82.56%
FIRST STAGE		10	16-Dec-26	29-Dec-26	17-Aug-26 A	23-Aug-26 A	84,594.16	0.00	84,594.16	0%	100%
DAM3-C-B9-M-300	Installation of Fire Fighting Pipes (Seamless Black Steel)	5	16-Dec-26	23-Dec-26	17-Aug-26 A	22-Aug-26 A	72,394.75	0.00	72,394.75	0%	100%
DAM3-C-B9-M-310	Installation of Fire Fighting Valve	5	24-Dec-26	29-Dec-26	17-Aug-26 A	23-Aug-26 A	12,199.40	0.00	12,199.40	0%	100%
SECOND STAGE		17	30-Dec-26	04-Jan-27	14-Dec-26	02-Jan-27	17,864.62	0.00	0.00	0%	0%
DAM3-C-B9-M-320	Installation of Fire Hose Cabinet	3	30-Dec-26	02-Jan-27	14-Dec-26	16-Dec-26	15,158.56	0.00	0.00	0%	0%
DAM3-C-B9-M-370	Supply, install, test and commission Fire Department Connection(FDC)	3	02-Jan-27	04-Jan-27	30-Dec-26	02-Jan-27	2,706.06	0.00	0.00	0%	0%
SEWER AND DRAINAGE SYSTEM		158	02-Jul-26	23-Dec-26	21-Jun-26 A	21-Dec-26	90,009.74	18,585.14	30,093.94	20.65%	33.43%
FIRST STAGE		158	02-Jul-26	07-Dec-26	21-Jun-26 A	05-Dec-26	41,149.90	18,585.14	30,093.94	45.16%	73.13%
DAM3-C-B9-M-200	Installation of Sanitary Waste / Drainage Pipes	4	02-Jul-26	06-Jul-26	21-Jun-26 A	24-Jun-26 A	18,585.14	18,585.14	18,585.14	100%	100%
DAM3-C-B9-M-380	Installation of Trench drain	5	02-Dec-26	07-Dec-26	22-Jun-26 A	24-Jun-26 A	11,508.80	0.00	11,508.80	0%	100%
DAM3-C-B9-M-220	Installation of Floor Drain	2	30-Nov-26	01-Dec-26	03-Dec-26	05-Dec-26	11,055.96	0.00	0.00	0%	0%
SECOND STAGE		14	08-Dec-26	23-Dec-26	06-Dec-26	21-Dec-26	48,859.84	0.00	0.00	0%	0%
DAM3-C-B9-M-180	Installation of Electric Water Heater	2	08-Dec-26	09-Dec-26	06-Dec-26	07-Dec-26	1,819.51	0.00	0.00	0%	0%
DAM3-C-B9-M-190	Installation of Sanitary Fixture and Accessories	4	10-Dec-26	14-Dec-26	08-Dec-26	12-Dec-26	19,921.72	0.00	0.00	0%	0%
DAM3-C-B9-M-210	Installation of Lavotary /Wash Basin	2	15-Dec-26	16-Dec-26	13-Dec-26	14-Dec-26	21,416.68	0.00	0.00	0%	0%
DAM3-C-B9-M-270	Installation of Bib Tap	2	17-Dec-26	19-Dec-26	15-Dec-26	16-Dec-26	1,900.66	0.00	0.00	0%	0%
DAM3-C-B9-M-428	Installation of Water Tap	2	20-Dec-26	21-Dec-26	17-Dec-26	19-Dec-26	2,874.14	0.00	0.00	0%	0%
DAM3-C-B9-M-429	Installation of Roof Vent Cap	2	22-Dec-26	23-Dec-26	20-Dec-26	21-Dec-26	927.12	0.00	0.00	0%	0%
WATER SUPPLY SYSTEM		8	16-Dec-26	28-Dec-26	14-Sep-26 A	19-Dec-26	41,870.81	0.00	41,592.68	0%	99.34%
FIRST STAGE		4	16-Dec-26	22-Dec-26	14-Sep-26 A	19-Sep-26 A	41,592.68	0.00	41,592.68	0%	100%
DAM3-C-B9-M-290	Installation of Water Supply Pipes	4	16-Dec-26	20-Dec-26	14-Sep-26 A	19-Sep-26 A	23,318.41	0.00	23,318.41	0%	100%
DAM3-C-B9-M-280	Installation of Water Supply Valve	2	21-Dec-26	22-Dec-26	15-Sep-26 A	19-Sep-26 A	18,274.27	0.00	18,274.27	0%	100%
SECOND STAGE		5	23-Dec-26	28-Dec-26	14-Dec-26	19-Dec-26	278.13	0.00	0.00	0%	0%
DAM3-C-B9-M-330	Capped connection	5	23-Dec-26	28-Dec-26	14-Dec-26	19-Dec-26	278.13	0.00	0.00	0%	0%
ELECTRICAL		77	21-Oct-26	31-Jan-27	20-May-26 A	13-Feb-27	752,044.76	0.00	27,642.87	0%	3.68%
FIRST STAGE		77	21-Oct-26	02-Dec-26	20-May-26 A	21-Dec-26	86,114.12	0.00	27,642.87	0%	32.1%
DAM3-C-B9-E-113	Installation of Earthing and Grounding	3	28-Nov-26	02-Dec-26	20-May-26 A	21-Dec-26	19,646.47	0.00	17,681.82	0%	90%
DAM3-C-B9-E-143	Installation of Conduits and wiring outlets - Fire Alarm System	4	21-Oct-26	25-Oct-26	21-May-26 A	22-Nov-26	1,768.31	0.00	884.15	0%	50%
DAM3-C-B9-E-183	Installation of Sleeves & Power outlet	8	21-Oct-26	29-Oct-26	21-May-26 A	24-Nov-26	2,920.45	0.00	1,460.23	0%	50%
DAM3-C-B9-E-163	Installation of Conduites for Lighting Fixture	4	04-Nov-26	08-Nov-26	08-Sep-26 A	02-Dec-26	8,462.97	0.00	7,616.67	0%	90%
DAM3-C-B9-E-233	Installation of Wires	4	09-Nov-26	12-Nov-26	02-Dec-26	07-Dec-26	16,925.94	0.00	0.00	0%	0%
DAM3-C-B9-E-223	Installation of LV Cables	4	23-Nov-26	26-Nov-26	16-Dec-26	21-Dec-26	36,389.98	0.00	0.00	0%	0%
SECOND STAGE		71	26-Oct-26	31-Jan-27	23-Nov-26	13-Feb-27	665,930.64	0.00	0.00	0%	0%
DAM3-C-B9-E-123	Installation of Fire Alarm Control Panel	4	26-Oct-26	29-Oct-26	23-Nov-26	26-Nov-26	19,451.37	0.00	0.00	0%	0%
DAM3-C-B9-E-133	Installation of Fire Detectors & Accessories	4	31-Oct-26	03-Nov-26	28-Nov-26	01-Dec-26	56,740.37	0.00	0.00	0%	0%
DAM3-C-B9-E-153	Installation of Lighting fixtures	4	14-Nov-26	17-Nov-26	07-Dec-26	12-Dec-26	76,166.74	0.00	0.00	0%	0%
DAM3-C-B9-E-193	Installation of Main Distribution Board	2	14-Nov-26	15-Nov-26	07-Dec-26	09-Dec-26	32,472.73	0.00	0.00	0%	0%
DAM3-C-B9-E-410	Installation of CCTV System	5	14-Nov-26	21-Nov-26	07-Dec-26	13-Dec-26	76,349.24	0.00	0.00	0%	0%
DAM3-C-B9-E-243	Installation of LP-1 Panel	2	16-Nov-26	17-Nov-26	09-Dec-26	12-Dec-26	18,403.54	0.00	0.00	0%	0%
DAM3-C-B9-E-253	Installation of PP-AC panel	2	18-Nov-26	19-Nov-26	12-Dec-26	14-Dec-26	21,648.48	0.00	0.00	0%	0%

Date	Revision	Checked	Approved
06-Oct-26	Weekly Report		

Activity ID	Activity Name	Original Duration	BL Project Start	BL Project Finish	Start	Finish	Budgeted Total Cost	Planned Value Cost	Earned Value Cost	Schedule % Complete	Performance % Complete
DAM3-C-B9-E-273	Installation of Access Control System	5	22-Nov-26	26-Nov-26	13-Dec-26	19-Dec-26	27,616.86	0.00	0.00	0%	0%
DAM3-C-B9-E-173	Installation of Wiring Devices	4	16-Dec-26	20-Dec-26	14-Dec-26	17-Dec-26	19,435.09	0.00	0.00	0%	0%
DAM3-C-B9-E-213	Installation of Telephone Cabinet	2	21-Nov-26	22-Nov-26	14-Dec-26	16-Dec-26	26,991.08	0.00	0.00	0%	0%
DAM3-C-B9-E-203	Installation of Disconnect Switches	2	21-Dec-26	22-Dec-26	19-Dec-26	20-Dec-26	30,235.95	0.00	0.00	0%	0%
DAM3-C-B9-E-283	Monitor Modules for Fire Alarm	2	28-Nov-26	29-Nov-26	19-Dec-26	21-Dec-26	3,882.38	0.00	0.00	0%	0%
DAM3-C-B9-E-293	Line Isolator Modules for Fire Alarm	2	30-Nov-26	01-Dec-26	21-Dec-26	23-Dec-26	185.40	0.00	0.00	0%	0%
DAM3-C-B9-E-303	Firewarning flash light with sounder; wall mounted, Weather proof	2	02-Dec-26	03-Dec-26	23-Dec-26	26-Dec-26	3,082.69	0.00	0.00	0%	0%
DAM3-C-B9-E-420	Installation of Solar power plant	8	16-Jan-27	31-Jan-27	03-Feb-27	13-Feb-27	253,268.71	0.00	0.00	0%	0%
BLOCK B10		293	03-Mar-26	08-Feb-27	18-Feb-26 A	18-Feb-27	5,075,523.09	2,496,308.73	3,221,399.98	49.18%	63.47%
STRUCTURAL		208	03-Mar-26	24-Oct-26	18-Feb-26 A	19-Nov-26	1,389,042.53	1,388,135.41	1,388,135.41	99.93%	99.93%
FOOTING		55	03-Mar-26	04-Apr-26	18-Feb-26 A	28-Apr-26 A	597,655.16	597,655.16	597,655.16	100%	100%
DAM3-C-B10-S-150	Excavation for footings	4	03-Mar-26	07-Mar-26	18-Feb-26 A	03-Mar-26 A	89,859.61	89,859.61	89,859.61	100%	100%
DAM3-C-B10-S-6323	Soil replacement - rock fill	4	08-Mar-26	11-Mar-26	07-Mar-26 A	11-Mar-26 A	179,061.91	179,061.91	179,061.91	100%	100%
DAM3-C-B10-S-6333	Engineering fill	4	12-Mar-26	16-Mar-26	18-Mar-26 A	31-Mar-26 A	46,046.19	46,046.19	46,046.19	100%	100%
DAM3-C-B10-S-103	Lean Concrete Below Footings	2	23-Mar-26	24-Mar-26	01-Apr-26 A	01-Apr-26 A	8,229.34	8,229.34	8,229.34	100%	100%
DAM3-C-B10-S-102	Vapour Barrier for Footings	1	22-Mar-26	22-Mar-26	01-Apr-26 A	01-Apr-26 A	7,940.10	7,940.10	7,940.10	100%	100%
DAM3-C-B10-S-101	Anti Termite Below Footings	1	21-Mar-26	21-Mar-26	01-Apr-26 A	01-Apr-26 A	11,905.55	11,905.55	11,905.55	100%	100%
DAM3-C-B10-S-104	Rebar for Footings	4	25-Mar-26	29-Mar-26	23-Apr-26 A	23-Apr-26 A	101,844.98	101,844.98	101,844.98	100%	100%
DAM3-C-B10-S-105	Formwork for Footings	4	30-Mar-26	02-Apr-26	23-Apr-26 A	25-Apr-26 A	25,461.25	25,461.25	25,461.25	100%	100%
DAM3-C-B10-S-106	Pouring Concrete for Footings	1	04-Apr-26	04-Apr-26	28-Apr-26 A	28-Apr-26 A	127,306.23	127,306.23	127,306.23	100%	100%
COLUMN NECK		17	05-Apr-26	22-Apr-26	26-Apr-26 A	20-May-26 A	120,554.54	120,554.54	120,554.54	100%	100%
DAM3-C-B10-S-257	Rebar for column neck	4	05-Apr-26	08-Apr-26	26-Apr-26 A	27-Apr-26 A	14,919.19	14,919.19	14,919.19	100%	100%
DAM3-C-B10-S-267	Formwork for column neck	2	09-Apr-26	11-Apr-26	27-Apr-26 A	04-May-26 A	9,946.13	9,946.13	9,946.13	100%	100%
DAM3-C-B10-S-297	Pouring Concrete for column neck	1	12-Apr-26	12-Apr-26	02-May-26 A	05-May-26 A	24,865.31	24,865.31	24,865.31	100%	100%
DAM3-C-B10-S-307	Damp proof /Bitumin paint on Footings & column neck	2	13-Apr-26	14-Apr-26	05-May-26 A	09-May-26 A	24,777.73	24,777.73	24,777.73	100%	100%
DAM3-C-B10-S-367	Backfilling / Compaction up to Bottom of Grade Beams	7	15-Apr-26	22-Apr-26	13-May-26 A	20-May-26 A	46,046.19	46,046.19	46,046.19	100%	100%
GRADE BEAM		16	23-Apr-26	13-May-26	25-May-26 A	15-Jun-26 A	171,632.86	171,632.86	171,632.86	100%	100%
DAM3-C-B10-S-338	Lean Concrete Below Grade Beams	2	27-Apr-26	28-Apr-26	25-May-26 A	25-May-26 A	4,431.19	4,431.19	4,431.19	100%	100%
DAM3-C-B10-S-337	Vapour barrier for Grade Beams	2	25-Apr-26	26-Apr-26	25-May-26 A	25-May-26 A	5,293.40	5,293.40	5,293.40	100%	100%
DAM3-C-B10-S-527	Anti Termite Below Grade Beams	1	23-Apr-26	23-Apr-26	25-May-26 A	25-May-26 A	11,905.55	11,905.55	11,905.55	100%	100%
DAM3-C-B10-S-339	Rebar for Grade Beams	5	29-Apr-26	04-May-26	31-May-26 A	03-Jun-26 A	27,194.46	27,194.46	27,194.46	100%	100%
DAM3-C-B10-S-341	Anchor bolts installation	2	05-May-26	06-May-26	02-Jun-26 A	03-Jun-26 A	57,238.83	57,238.83	57,238.83	100%	100%
DAM3-C-B10-S-340	Formwork for Grade Beams	2	05-May-26	06-May-26	07-Jun-26 A	09-Jun-26 A	6,798.61	6,798.61	6,798.61	100%	100%
DAM3-C-B10-S-342	Pouring Concrete for Grade Beams	1	07-May-26	07-May-26	09-Jun-26 A	09-Jun-26 A	33,993.09	33,993.09	33,993.09	100%	100%
DAM3-C-B10-S-347	Damp proof /Bitumin paint on Grade Beams	5	09-May-26	13-May-26	14-Jun-26 A	15-Jun-26 A	24,777.73	24,777.73	24,777.73	100%	100%
SLAB ON GRADE		121	14-May-26	24-Oct-26	16-Jun-26 A	19-Nov-26	397,232.98	396,325.87	396,325.87	99.77%	99.77%
DAM3-C-B10-S-377	Backfilling / Compaction for Slab on Grade	7	14-May-26	21-May-26	16-Jun-26 A	22-Jun-26 A	23,023.09	23,023.09	23,023.09	100%	100%
DAM3-C-B10-S-382	Pouring Concrete for Ground Slab	4	30-May-26	02-Jun-26	18-Jul-26 A	21-Jul-26 A	344,195.21	344,195.21	344,195.21	100%	100%
DAM3-C-B10-S-378	Anti Termite Treatment below Ground Slab	1	23-May-26	23-May-26	18-Jul-26 A	21-Jul-26 A	15,874.08	15,874.08	15,874.08	100%	100%
DAM3-C-B10-S-379	Vapour barrier for below Ground Slab	2	24-May-26	25-May-26	18-Jul-26 A	21-Jul-26 A	13,233.49	13,233.49	13,233.49	100%	100%
DAM3-C-B10-S-517	Concrete pad	7	17-Oct-26	24-Oct-26	12-Nov-26	19-Nov-26	907.11	0.00	0.00	0%	0%
COLUMNS & BEAMS		55	23-May-26	22-Jun-26	01-Jun-26 A	16-Sep-26 A	101,966.98	101,966.98	101,966.98	100%	100%
DAM3-C-B10-S-6101	Rebar for Tie Beams	4	07-Jun-26	10-Jun-26	01-Jun-26 A	03-Jun-26 A	7,263.64	7,263.64	7,263.64	100%	100%
DAM3-C-B10-S-6102	Formwork for Tie Beams	2	11-Jun-26	13-Jun-26	07-Jun-26 A	08-Jun-26 A	1,815.91	1,815.91	1,815.91	100%	100%
DAM3-C-B10-S-6103	Pouring Concrete for Tie Beams	1	14-Jun-26	14-Jun-26	09-Jun-26 A	09-Jun-26 A	9,079.54	9,079.54	9,079.54	100%	100%
DAM3-C-B10-S-5101	Rebar for column	5	23-May-26	31-May-26	12-Jul-26 A	16-Jul-26 A	20,144.05	20,144.05	20,144.05	100%	100%
DAM3-C-B10-S-5102	Formwork for column	4	01-Jun-26	04-Jun-26	04-Aug-26 A	06-Aug-26 A	5,036.01	5,036.01	5,036.01	100%	100%
DAM3-C-B10-S-5103	Pouring Concrete for column	1	06-Jun-26	06-Jun-26	05-Aug-26 A	09-Aug-26 A	25,180.06	25,180.06	25,180.06	100%	100%
DAM3-C-B10-S-6113	Rebar for Beams	4	15-Jun-26	18-Jun-26	31-Aug-26 A	02-Sep-26 A	13,379.11	13,379.11	13,379.11	100%	100%

2026 2027

Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary


Date	Revision	Checked	Approved
06-Oct-26	Weekly Report		

Activity ID	Activity Name	Original Duration	BL Project Start	BL Project Finish	Start	Finish	Budgeted Total Cost	Planned Value Cost	Earned Value Cost	Schedule % Complete	Performance % Complete
DAM3-C-B10-S-6123	Formwork for Beams	2	20-Jun-26	21-Jun-26	08-Sep-26 A	15-Sep-26 A	3,344.77	3,344.77	3,344.77	100%	100%
DAM3-C-B10-S-6133	Pouring Concrete for Beams	1	22-Jun-26	22-Jun-26	12-Sep-26 A	16-Sep-26 A	16,723.88	16,723.88	16,723.88	100%	100%
STRUCTURAL STEEL		48	12-Sep-26	21-Oct-26	25-Jun-26 A	19-Nov-26	1,566,668.48	1,031,249.45	1,535,105.59	65.82%	97.99%
DAM3-C-B10-SS-0100	Installation of columns	3	12-Sep-26	14-Sep-26	25-Jun-26 A	25-Jun-26 A	217,507.55	217,507.55	217,507.55	100%	100%
DAM3-C-B10-SS-0110	Installation of raft and purlins	5	15-Sep-26	20-Sep-26	25-Jun-26 A	28-Jun-26 A	326,261.32	326,261.32	326,261.32	100%	100%
DAM3-C-B10-SS-610	Intumescent paint to steel works	7	21-Sep-26	29-Sep-26	07-Jul-26 A	11-Aug-26 A	317,759.56	317,759.56	317,759.56	100%	100%
DAM3-C-B10-SS-0140	Installation of roof sheet	3	04-Oct-26	08-Oct-26	13-Aug-26 A	16-Aug-26 A	217,507.55	87,003.02	217,507.55	40%	100%
DAM3-C-B10-SS-0130	Installation of wall sandwich panel	5	17-Oct-26	21-Oct-26	03-Sep-26 A	30-Sep-26 A	326,261.32	0.00	326,261.32	0%	100%
DAM3-C-B10-SS-1030	Steel members for external platform	7	08-Oct-26	15-Oct-26	26-Sep-26 A	14-Nov-26	18,670.78	0.00	14,003.08	0%	75%
DAM3-C-B10-SS-620	Steel members for office area	4	30-Sep-26	07-Oct-26	29-Sep-26 A	30-Sep-26 A	115,805.20	82,718.00	115,805.20	71.43%	100%
DAM3-C-B10-SS-1020	Epoxy paint to steel members at office area	4	08-Oct-26	15-Oct-26	12-Nov-26	16-Nov-26	23,161.04	0.00	0.00	0%	0%
DAM3-C-B10-SS-1040	Epoxy paint for external platform	5	17-Oct-26	21-Oct-26	14-Nov-26	19-Nov-26	3,734.16	0.00	0.00	0%	0%
ARCHITECTURAL		81	21-Sep-26	16-Jan-27	23-Jul-26 A	07-Jan-27	900,244.66	58,338.72	121,851.99	6.48%	13.54%
MASONARY WORKS		20	21-Sep-26	24-Oct-26	02-Aug-26 A	03-Sep-26 A	78,954.21	58,338.72	78,954.21	73.89%	100%
DAM3-C-B10-A-0120	Block work at factory area	3	21-Sep-26	03-Oct-26	02-Aug-26 A	23-Aug-26 A	58,338.72	58,338.72	58,338.72	100%	100%
DAM3-C-B10-A-0150	Block work at office area	4	08-Oct-26	15-Oct-26	08-Aug-26 A	01-Sep-26 A	6,179.18	0.00	6,179.18	0%	100%
DAM3-C-B10-A-170	Block work at toilet area	5	17-Oct-26	24-Oct-26	11-Aug-26 A	03-Sep-26 A	14,436.31	0.00	14,436.31	0%	100%
WALL FINISHES		29	03-Nov-26	19-Dec-26	21-Sep-26 A	21-Dec-26	92,757.47	0.00	36,442.62	0%	39.29%
DAM3-C-B10-A-180	Internal Wall Plaster	5	03-Nov-26	19-Nov-26	21-Sep-26 A	22-Nov-26	48,590.16	0.00	36,442.62	0%	75%
DAM3-C-B10-A-230	Paint to Plaster (Primer, Putty & First Coat)	5	12-Dec-26	19-Dec-26	16-Dec-26	21-Dec-26	44,167.30	0.00	0.00	0%	0%
CIELING FINISHES		4	03-Dec-26	08-Dec-26	14-Dec-26	17-Dec-26	46,792.30	0.00	0.00	0%	0%
DAM3-C-B10-A-240	Installation of Ceiling Gypsum Board	4	03-Dec-26	08-Dec-26	14-Dec-26	17-Dec-26	46,792.30	0.00	0.00	0%	0%
FLOOR FINISHES		27	25-Nov-26	16-Jan-27	08-Dec-26	07-Jan-27	189,488.90	0.00	0.00	0%	0%
DAM3-C-B10-A-220	Tiles for Toilet	5	25-Nov-26	02-Dec-26	08-Dec-26	13-Dec-26	46,530.71	0.00	0.00	0%	0%
DAM3-C-B10-A-250	Tiles for Office Area	2	09-Dec-26	10-Dec-26	14-Dec-26	15-Dec-26	26,867.31	0.00	0.00	0%	0%
DAM3-C-B10-A-390	Granite strip	2	12-Dec-26	13-Dec-26	16-Dec-26	17-Dec-26	671.12	0.00	0.00	0%	0%
DAM3-C-B10-A-420	Epoxy paint	3	09-Jan-27	16-Jan-27	05-Jan-27	07-Jan-27	115,419.76	0.00	0.00	0%	0%
DOORS & WINDOWS		14	22-Oct-26	07-Nov-26	17-Nov-26	02-Dec-26	248,575.06	0.00	0.00	0%	0%
DAM3-C-B10-A-552	Window (CW1)	7	22-Oct-26	29-Oct-26	17-Nov-26	24-Nov-26	94,173.21	0.00	0.00	0%	0%
DAM3-C-B10-A-553	Roll up Shutter Door	1	31-Oct-26	31-Oct-26	25-Nov-26	25-Nov-26	68,619.20	0.00	0.00	0%	0%
DAM3-C-B10-A-200	Supply and install (D5) 1000*2200mm single leaf steel door with door	1	01-Nov-26	01-Nov-26	26-Nov-26	26-Nov-26	16,016.16	0.00	0.00	0%	0%
DAM3-C-B10-A-554	Supply and install (D4) 800*2200 mm single leaf aluminum door with door	1	02-Nov-26	02-Nov-26	28-Nov-26	28-Nov-26	22,737.85	0.00	0.00	0%	0%
DAM3-C-B10-A-555	Supply and install (D7) 1000*2200 mm single leaf aluminum door with door	1	03-Nov-26	03-Nov-26	29-Nov-26	29-Nov-26	7,811.07	0.00	0.00	0%	0%
DAM3-C-B10-A-556	Supply and install (D3) 1000*2200 mm single leaf aluminum door with door	1	04-Nov-26	04-Nov-26	30-Nov-26	30-Nov-26	16,016.16	0.00	0.00	0%	0%
DAM3-C-B10-A-557	Supply and install fire rated 45 min (D2) 1200*2200 mm single leaf steel doo	1	05-Nov-26	05-Nov-26	01-Dec-26	01-Dec-26	16,711.52	0.00	0.00	0%	0%
DAM3-C-B10-A-558	Skylight fixtures installation	1	07-Nov-26	07-Nov-26	02-Dec-26	02-Dec-26	6,489.89	0.00	0.00	0%	0%
WATER PROOFING WORKS		4	21-Nov-26	24-Nov-26	03-Dec-26	07-Dec-26	4,879.02	0.00	0.00	0%	0%
DAM3-C-B10-A-370	Waterproofing membrane for toilets	4	21-Nov-26	24-Nov-26	03-Dec-26	07-Dec-26	4,879.02	0.00	0.00	0%	0%
METAL WORKS		54	14-Dec-26	28-Dec-26	23-Jul-26 A	27-Dec-26	193,717.06	0.00	6,455.16	0%	3.33%
DAM3-C-B10-A-300	Galvanised Steel Gratings	2	27-Dec-26	28-Dec-26	23-Jul-26 A	23-Jul-26 A	6,455.16	0.00	6,455.16	0%	100%
DAM3-C-B10-A-290	Steel Ladder	2	14-Dec-26	15-Dec-26	19-Dec-26	20-Dec-26	9,839.16	0.00	0.00	0%	0%
DAM3-C-B10-A-291	Steel railing works	3	16-Dec-26	20-Dec-26	21-Dec-26	23-Dec-26	1,533.98	0.00	0.00	0%	0%
DAM3-C-B10-A-292	Aluminium composite panel	3	21-Dec-26	26-Dec-26	24-Dec-26	27-Dec-26	175,888.76	0.00	0.00	0%	0%
SPECIALTIES		7	29-Dec-26	07-Jan-27	28-Dec-26	04-Jan-27	45,080.66	0.00	0.00	0%	0%
DAM3-C-B10-A-320	Installation of fittings	3	29-Dec-26	03-Jan-27	28-Dec-26	30-Dec-26	22,981.27	0.00	0.00	0%	0%
DAM3-C-B10-A-570	Identification sign; ID01 & ID02	3	04-Jan-27	06-Jan-27	31-Dec-26	03-Jan-27	9,630.56	0.00	0.00	0%	0%
DAM3-C-B10-A-340	Furniture Installation	1	07-Jan-27	07-Jan-27	04-Jan-27	04-Jan-27	12,468.83	0.00	0.00	0%	0%
MECHANICAL		168	14-May-26	07-Jan-27	01-Jul-26 A	10-Jan-27	467,522.66	18,585.14	156,280.78	3.98%	33.43%
HVAC		14	20-Dec-26	04-Jan-27	22-Dec-26	06-Jan-27	233,183.33	0.00	0.00	0%	0%

Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary

Date	Revision	Checked	Approved
06-Oct-26	Weekly Report		

Activity ID	Activity Name	Original Duration	BL Project Start	BL Project Finish	Start	Finish	Budgeted Total Cost	Planned Value Cost	Earned Value Cost	Schedule % Complete	Performance % Complete
FIRST STAGE		4	27-Dec-26	30-Dec-26	29-Dec-26	02-Jan-27	170,694.73	0.00	0.00	0%	0%
DAM3-C-B10-M-140	Installation of HVAC Ducts	2	27-Dec-26	28-Dec-26	29-Dec-26	30-Dec-26	149,489.33	0.00	0.00	0%	0%
DAM3-C-B10-M-170	Installation of Duct insulation	2	29-Dec-26	30-Dec-26	31-Dec-26	02-Jan-27	21,205.40	0.00	0.00	0%	0%
SECOND STAGE		14	20-Dec-26	04-Jan-27	22-Dec-26	06-Jan-27	62,488.60	0.00	0.00	0%	0%
DAM3-C-B10-M-130	Installation of Exhaust Fans	2	20-Dec-26	21-Dec-26	22-Dec-26	23-Dec-26	7,938.56	0.00	0.00	0%	0%
DAM3-C-B10-M-160	Installation of Wall Propeller Type Exhaust Fan	4	22-Dec-26	26-Dec-26	24-Dec-26	28-Dec-26	46,831.64	0.00	0.00	0%	0%
DAM3-C-B10-M-339	Installation of Diffuser	2	31-Dec-26	02-Jan-27	03-Jan-27	04-Jan-27	2,144.00	0.00	0.00	0%	0%
DAM3-C-B10-M-340	Supply, install, test and commission door grilles & exhaust louvers	2	03-Jan-27	04-Jan-27	05-Jan-27	06-Jan-27	5,574.40	0.00	0.00	0%	0%
FIRE FIGHTING SYSTEM		21	20-Dec-26	07-Jan-27	23-Aug-26 A	10-Jan-27	102,458.78	0.00	84,594.16	0%	82.56%
FIRST STAGE		8	20-Dec-26	02-Jan-27	23-Aug-26 A	29-Aug-26 A	84,594.16	0.00	84,594.16	0%	100%
DAM3-C-B10-M-300	Installation of Fire Fighting Pipes (Seamless Black Steel)	7	20-Dec-26	27-Dec-26	23-Aug-26 A	27-Aug-26 A	72,394.75	0.00	72,394.75	0%	100%
DAM3-C-B10-M-310	Installation of Fire Fighting Valve	3	28-Dec-26	02-Jan-27	25-Aug-26 A	29-Aug-26 A	12,199.40	0.00	12,199.40	0%	100%
SECOND STAGE		17	03-Jan-27	07-Jan-27	22-Dec-26	10-Jan-27	17,864.62	0.00	0.00	0%	0%
DAM3-C-B10-M-320	Installation of Fire Hose Cabinet	3	03-Jan-27	05-Jan-27	22-Dec-26	24-Dec-26	15,158.56	0.00	0.00	0%	0%
DAM3-C-B10-M-370	Supply, install, test and commission Fire Department Connection(FDC)	3	05-Jan-27	07-Jan-27	07-Jan-27	10-Jan-27	2,706.06	0.00	0.00	0%	0%
SEWER AND DRAINAGE SYSTEM		168	14-May-26	27-Dec-26	01-Jul-26 A	31-Dec-26	90,009.74	18,585.14	30,093.94	20.65%	33.43%
FIRST STAGE		168	14-May-26	10-Dec-26	01-Jul-26 A	15-Dec-26	41,149.90	18,585.14	30,093.94	45.16%	73.13%
DAM3-C-B10-M-200	Installation of Sanitary Waste / Drainage Pipes	4	14-May-26	18-May-26	01-Jul-26 A	06-Jul-26 A	18,585.14	18,585.14	18,585.14	100%	100%
DAM3-C-B10-M-380	Installation of Trench drain	5	06-Dec-26	10-Dec-26	07-Jul-26 A	09-Jul-26 A	11,508.80	0.00	11,508.80	0%	100%
DAM3-C-B10-M-220	Installation of Floor Drain	2	03-Dec-26	05-Dec-26	14-Dec-26	15-Dec-26	11,055.96	0.00	0.00	0%	0%
SECOND STAGE		14	12-Dec-26	27-Dec-26	16-Dec-26	31-Dec-26	48,859.84	0.00	0.00	0%	0%
DAM3-C-B10-M-180	Installation of Electric Water Heater	2	12-Dec-26	13-Dec-26	16-Dec-26	17-Dec-26	1,819.51	0.00	0.00	0%	0%
DAM3-C-B10-M-190	Installation of Sanitary Fixture and Accessories	4	14-Dec-26	17-Dec-26	19-Dec-26	22-Dec-26	19,921.72	0.00	0.00	0%	0%
DAM3-C-B10-M-210	Installation of Lavotary /Wash Basin	2	19-Dec-26	20-Dec-26	23-Dec-26	24-Dec-26	21,416.68	0.00	0.00	0%	0%
DAM3-C-B10-M-270	Installation of Bib Tap	2	21-Dec-26	22-Dec-26	26-Dec-26	27-Dec-26	1,900.66	0.00	0.00	0%	0%
DAM3-C-B10-M-428	Installation of Water Tap	2	23-Dec-26	24-Dec-26	28-Dec-26	29-Dec-26	2,874.14	0.00	0.00	0%	0%
DAM3-C-B10-M-429	Installation of Roof Vent Cap	2	26-Dec-26	27-Dec-26	30-Dec-26	31-Dec-26	927.12	0.00	0.00	0%	0%
WATER SUPPLY SYSTEM		9	20-Dec-26	31-Dec-26	17-Sep-26 A	27-Dec-26	41,870.81	0.00	41,592.68	0%	99.34%
FIRST STAGE		6	20-Dec-26	26-Dec-26	17-Sep-26 A	21-Sep-26 A	41,592.68	0.00	41,592.68	0%	100%
DAM3-C-B10-M-280	Installation of Water Supply Valve	2	24-Dec-26	26-Dec-26	17-Sep-26 A	21-Sep-26 A	18,274.27	0.00	18,274.27	0%	100%
DAM3-C-B10-M-290	Installation of Water Supply Pipes	4	20-Dec-26	23-Dec-26	17-Sep-26 A	21-Sep-26 A	23,318.41	0.00	23,318.41	0%	100%
SECOND STAGE		5	27-Dec-26	31-Dec-26	22-Dec-26	27-Dec-26	278.13	0.00	0.00	0%	0%
DAM3-C-B10-M-330	Capped connection	5	27-Dec-26	31-Dec-26	22-Dec-26	27-Dec-26	278.13	0.00	0.00	0%	0%
ELECTRICAL		90	25-Oct-26	08-Feb-27	02-Jun-26 A	18-Feb-27	752,044.76	0.00	20,026.20	0%	2.66%
FIRST STAGE		82	25-Oct-26	06-Dec-26	02-Jun-26 A	17-Dec-26	86,114.12	0.00	20,026.20	0%	23.26%
DAM3-C-B10-E-113	Installation of Earthing and Grounding	5	01-Dec-26	06-Dec-26	02-Jun-26 A	17-Dec-26	19,646.47	0.00	17,681.82	0%	90%
DAM3-C-B10-E-143	Installation of Conduits and wiring outlets - Fire Alarm System	4	25-Oct-26	28-Oct-26	03-Jun-26 A	14-Nov-26	1,768.31	0.00	884.15	0%	50%
DAM3-C-B10-E-183	Installation of Sleeves & Power outlet	4	25-Oct-26	02-Nov-26	03-Jun-26 A	14-Nov-26	2,920.45	0.00	1,460.23	0%	50%
DAM3-C-B10-E-163	Installation of Conduites for Lighting Fixture	4	08-Nov-26	11-Nov-26	24-Nov-26	28-Nov-26	8,462.97	0.00	0.00	0%	0%
DAM3-C-B10-E-233	Installation of Wires	4	12-Nov-26	16-Nov-26	29-Nov-26	02-Dec-26	16,925.94	0.00	0.00	0%	0%
DAM3-C-B10-E-223	Installation of LV Cables	4	26-Nov-26	30-Nov-26	13-Dec-26	16-Dec-26	36,389.98	0.00	0.00	0%	0%
SECOND STAGE		83	29-Oct-26	08-Feb-27	15-Nov-26	18-Feb-27	665,930.64	0.00	0.00	0%	0%
DAM3-C-B10-E-123	Installation of Fire Alarm Control Panel	4	29-Oct-26	02-Nov-26	15-Nov-26	18-Nov-26	19,451.37	0.00	0.00	0%	0%
DAM3-C-B10-E-133	Installation of Fire Detectors & Accessories	4	03-Nov-26	07-Nov-26	19-Nov-26	23-Nov-26	56,740.37	0.00	0.00	0%	0%
DAM3-C-B10-E-153	Installation of Lighting fixtures	4	17-Nov-26	21-Nov-26	03-Dec-26	07-Dec-26	76,166.74	0.00	0.00	0%	0%
DAM3-C-B10-E-193	Installation of Main Distribution Board	2	17-Nov-26	18-Nov-26	03-Dec-26	05-Dec-26	32,472.73	0.00	0.00	0%	0%
DAM3-C-B10-E-410	Installation of CCTV System	7	17-Nov-26	24-Nov-26	03-Dec-26	10-Dec-26	76,349.24	0.00	0.00	0%	0%
DAM3-C-B10-E-243	Installation of LP-1 Panel	2	19-Nov-26	21-Nov-26	06-Dec-26	07-Dec-26	18,403.54	0.00	0.00	0%	0%
DAM3-C-B10-E-253	Installation of PP-AC panel	2	22-Nov-26	23-Nov-26	08-Dec-26	09-Dec-26	21,648.48	0.00	0.00	0%	0%




Actual Level of Effort | Remaining Work | Milestone
Actual Work | Critical Remaining Work | summary

Date	Revision	Checked	Approved
06-Oct-26	Weekly Report		

Activity ID	Activity Name	Original Duration	BL Project Start	BL Project Finish	Start	Finish	Budgeted Total Cost	Planned Value Cost	Earned Value Cost	Schedule % Complete	Performance % Complete
DAM3-C-B10-E-213	Installation of Telephone Cabinet	2	24-Nov-26	25-Nov-26	10-Dec-26	12-Dec-26	26,991.08	0.00	0.00	0%	0%
DAM3-C-B10-E-273	Installation of Access Control System	5	25-Nov-26	30-Nov-26	12-Dec-26	16-Dec-26	27,616.86	0.00	0.00	0%	0%
DAM3-C-B10-E-283	Monitor Modules for Fire Alarm	2	01-Dec-26	02-Dec-26	17-Dec-26	19-Dec-26	3,882.38	0.00	0.00	0%	0%
DAM3-C-B10-E-293	Line Isolator Modules for Fire Alarm	2	03-Dec-26	05-Dec-26	20-Dec-26	21-Dec-26	185.40	0.00	0.00	0%	0%
DAM3-C-B10-E-173	Installation of Wiring Devices	4	20-Dec-26	23-Dec-26	22-Dec-26	26-Dec-26	19,435.09	0.00	0.00	0%	0%
DAM3-C-B10-E-303	Firewarning flash light with sounder; wall mounted, Weather proof	2	06-Dec-26	07-Dec-26	22-Dec-26	23-Dec-26	3,082.69	0.00	0.00	0%	0%
DAM3-C-B10-E-203	Installation of Disconnect Switches	2	24-Dec-26	26-Dec-26	27-Dec-26	28-Dec-26	30,235.95	0.00	0.00	0%	0%
DAM3-C-B10-E-420	Installation of Solar power plant	5	01-Feb-27	08-Feb-27	13-Feb-27	18-Feb-27	253,268.71	0.00	0.00	0%	0%
BLOCK B11		288	08-Mar-26	16-Feb-27	18-Feb-26 A	24-Feb-27	5,075,523.09	2,353,841.04	3,141,509.13	46.38%	61.9%
STRUCTURAL		202	08-Mar-26	27-Oct-26	18-Feb-26 A	19-Nov-26	1,389,042.53	1,388,135.41	1,388,135.41	99.93%	99.93%
FOOTING		36	08-Mar-26	08-Apr-26	18-Feb-26 A	02-May-26 A	597,655.16	597,655.16	597,655.16	100%	100%
DAM3-C-B11-S-150	Excavation for footings	4	08-Mar-26	11-Mar-26	18-Feb-26 A	08-Mar-26 A	89,859.61	89,859.61	89,859.61	100%	100%
DAM3-C-B11-S-6343	Soil replacement - rock fill	4	12-Mar-26	16-Mar-26	08-Mar-26 A	16-Mar-26 A	179,061.91	179,061.91	179,061.91	100%	100%
DAM3-C-B11-S-6353	Engineering fill	4	21-Mar-26	24-Mar-26	26-Mar-26 A	31-Mar-26 A	46,046.19	46,046.19	46,046.19	100%	100%
DAM3-C-B11-S-103	Lean Concrete Below Footings	2	28-Mar-26	29-Mar-26	02-Apr-26 A	02-Apr-26 A	8,229.34	8,229.34	8,229.34	100%	100%
DAM3-C-B11-S-102	Vapour Barrier for Footings	1	26-Mar-26	26-Mar-26	02-Apr-26 A	02-Apr-26 A	7,940.10	7,940.10	7,940.10	100%	100%
DAM3-C-B11-S-101	Anti Termite Below Footings	1	25-Mar-26	25-Mar-26	02-Apr-26 A	02-Apr-26 A	11,905.55	11,905.55	11,905.55	100%	100%
DAM3-C-B11-S-104	Rebar for Footings	4	30-Mar-26	02-Apr-26	25-Apr-26 A	28-Apr-26 A	101,844.98	101,844.98	101,844.98	100%	100%
DAM3-C-B11-S-105	Formwork for Footings	4	04-Apr-26	07-Apr-26	28-Apr-26 A	29-Apr-26 A	25,461.25	25,461.25	25,461.25	100%	100%
DAM3-C-B11-S-106	Pouring Concrete for Footings	1	08-Apr-26	08-Apr-26	02-May-26 A	02-May-26 A	127,306.23	127,306.23	127,306.23	100%	100%
COLUMN NECK		19	09-Apr-26	27-Apr-26	27-Apr-26 A	20-May-26 A	120,554.54	120,554.54	120,554.54	100%	100%
DAM3-C-B11-S-257	Rebar for column neck	4	09-Apr-26	13-Apr-26	27-Apr-26 A	28-Apr-26 A	14,919.19	14,919.19	14,919.19	100%	100%
DAM3-C-B11-S-267	Formwork for column neck	2	14-Apr-26	15-Apr-26	05-May-26 A	06-May-26 A	9,946.13	9,946.13	9,946.13	100%	100%
DAM3-C-B11-S-297	Pouring Concrete for column neck	1	16-Apr-26	16-Apr-26	07-May-26 A	07-May-26 A	24,865.31	24,865.31	24,865.31	100%	100%
DAM3-C-B11-S-307	Damp proof /Bitumin paint on Footings & column neck	2	18-Apr-26	19-Apr-26	11-May-26 A	13-May-26 A	24,777.73	24,777.73	24,777.73	100%	100%
DAM3-C-B11-S-367	Backfilling / Compaction up to Bottom of Grade Beams	7	20-Apr-26	27-Apr-26	17-May-26 A	20-May-26 A	46,046.19	46,046.19	46,046.19	100%	100%
GRADE BEAM		18	28-Apr-26	18-May-26	24-May-26 A	13-Jun-26 A	171,632.86	171,632.86	171,632.86	100%	100%
DAM3-C-B11-S-338	Lean Concrete Below Grade Beams	2	02-May-26	03-May-26	24-May-26 A	24-May-26 A	4,431.19	4,431.19	4,431.19	100%	100%
DAM3-C-B11-S-337	Vapour barrier for Grade Beams	2	29-Apr-26	30-Apr-26	24-May-26 A	24-May-26 A	5,293.40	5,293.40	5,293.40	100%	100%
DAM3-C-B11-S-527	Anti Termite Below Grade Beams	1	28-Apr-26	28-Apr-26	24-May-26 A	24-May-26 A	11,905.55	11,905.55	11,905.55	100%	100%
DAM3-C-B11-S-339	Rebar for Grade Beams	5	04-May-26	09-May-26	01-Jun-26 A	03-Jun-26 A	27,194.46	27,194.46	27,194.46	100%	100%
DAM3-C-B11-S-340	Formwork for Grade Beams	2	10-May-26	11-May-26	02-Jun-26 A	06-Jun-26 A	6,798.61	6,798.61	6,798.61	100%	100%
DAM3-C-B11-S-341	Anchor bolts installation	2	10-May-26	11-May-26	02-Jun-26 A	03-Jun-26 A	57,238.83	57,238.83	57,238.83	100%	100%
DAM3-C-B11-S-342	Pouring Concrete for Grade Beams	1	12-May-26	12-May-26	06-Jun-26 A	06-Jun-26 A	33,993.09	33,993.09	33,993.09	100%	100%
DAM3-C-B11-S-347	Damp proof /Bitumin paint on Grade Beams	5	13-May-26	18-May-26	11-Jun-26 A	13-Jun-26 A	24,777.73	24,777.73	24,777.73	100%	100%
SLAB ON GRADE		134	19-May-26	27-Oct-26	15-Jun-26 A	19-Nov-26	397,232.98	396,325.87	396,325.87	99.77%	99.77%
DAM3-C-B11-S-377	Backfilling / Compaction for Slab on Grade	7	19-May-26	30-May-26	15-Jun-26 A	21-Jun-26 A	23,023.09	23,023.09	23,023.09	100%	100%
DAM3-C-B11-S-382	Pouring Concrete for Ground Slab	4	03-Jun-26	07-Jun-26	26-Jul-26 A	28-Jul-26 A	344,195.21	344,195.21	344,195.21	100%	100%
DAM3-C-B11-S-378	Anti Termite Treatment below Ground Slab	1	31-May-26	31-May-26	26-Jul-26 A	28-Jul-26 A	15,874.08	15,874.08	15,874.08	100%	100%
DAM3-C-B11-S-379	Vapour barrier for below Ground Slab	2	01-Jun-26	02-Jun-26	26-Jul-26 A	28-Jul-26 A	13,233.49	13,233.49	13,233.49	100%	100%
DAM3-C-B11-S-517	Concrete pad	7	20-Oct-26	27-Oct-26	12-Nov-26	19-Nov-26	907.11	0.00	0.00	0%	0%
COLUMNS & BEAMS		81	31-May-26	27-Jun-26	02-Jun-26 A	01-Oct-26 A	101,966.98	101,966.98	101,966.98	100%	100%
DAM3-C-B11-S-6101	Rebar for Tie Beams	4	11-Jun-26	15-Jun-26	02-Jun-26 A	08-Jun-26 A	7,263.64	7,263.64	7,263.64	100%	100%
DAM3-C-B11-S-6102	Formwork for Tie Beams	2	16-Jun-26	17-Jun-26	03-Jun-26 A	08-Jun-26 A	1,815.91	1,815.91	1,815.91	100%	100%
DAM3-C-B11-S-6103	Pouring Concrete for Tie Beams	1	18-Jun-26	18-Jun-26	06-Jun-26 A	09-Jun-26 A	9,079.54	9,079.54	9,079.54	100%	100%
DAM3-C-B11-S-5101	Rebar for column	5	31-May-26	04-Jun-26	13-Jul-26 A	16-Jul-26 A	20,144.05	20,144.05	20,144.05	100%	100%
DAM3-C-B11-S-5102	Formwork for column	4	06-Jun-26	09-Jun-26	08-Aug-26 A	11-Aug-26 A	5,036.01	5,036.01	5,036.01	100%	100%
DAM3-C-B11-S-5103	Pouring Concrete for column	1	10-Jun-26	10-Jun-26	09-Aug-26 A	12-Aug-26 A	25,180.06	25,180.06	25,180.06	100%	100%
DAM3-C-B11-S-6113	Rebar for Beams	4	20-Jun-26	23-Jun-26	01-Sep-26 A	03-Sep-26 A	13,379.11	13,379.11	13,379.11	100%	100%

Activity ID	Activity Name	Original Duration	BL Project Start	BL Project Finish	Start	Finish	Budgeted Total Cost	Planned Value Cost	Earned Value Cost	Schedule % Complete	Performance % Complete
DAM3-C-B11-S-6123	Formwork for Beams	2	24-Jun-26	25-Jun-26	21-Sep-26 A	26-Sep-26 A	3,344.77	3,344.77	3,344.77	100%	100%
DAM3-C-B11-S-6133	Pouring Concrete for Beams	1	27-Jun-26	27-Jun-26	28-Sep-26 A	01-Oct-26 A	16,723.88	16,723.88	16,723.88	100%	100%
STRUCTURAL STEEL		44	15-Sep-26	25-Oct-26	25-Jun-26 A	25-Nov-26	1,566,668.48	894,615.63	1,521,102.51	57.1%	97.09%
DAM3-C-B11-SS-0100	Installation of columns	3	15-Sep-26	17-Sep-26	25-Jun-26 A	28-Jun-26 A	217,507.55	217,507.55	217,507.55	100%	100%
DAM3-C-B11-SS-0110	Installation of raft and purlins	5	19-Sep-26	24-Sep-26	30-Jun-26 A	01-Jul-26 A	326,261.32	326,261.32	326,261.32	100%	100%
DAM3-C-B11-SS-610	Intumescent paint to steel works	7	26-Sep-26	03-Oct-26	19-Jul-26 A	25-Jul-26 A	317,759.56	317,759.56	317,759.56	100%	100%
DAM3-C-B11-SS-0140	Installation of roof sheet	5	07-Oct-26	12-Oct-26	01-Aug-26 A	08-Aug-26 A	217,507.55	0.00	217,507.55	0%	100%
DAM3-C-B11-SS-0130	Installation of wall sandwich panel	5	20-Oct-26	25-Oct-26	03-Sep-26 A	30-Sep-26 A	326,261.32	0.00	326,261.32	0%	100%
DAM3-C-B11-SS-620	Steel members for office area	7	04-Oct-26	11-Oct-26	27-Sep-26 A	30-Sep-26 A	115,805.20	33,087.20	115,805.20	28.57%	100%
DAM3-C-B11-SS-1020	Epoxy paint to steel members at office area	4	12-Oct-26	19-Oct-26	12-Nov-26	16-Nov-26	23,161.04	0.00	0.00	0%	0%
DAM3-C-B11-SS-1030	Steel members for external platform	7	12-Oct-26	19-Oct-26	12-Nov-26	19-Nov-26	18,670.78	0.00	0.00	0%	0%
DAM3-C-B11-SS-1040	Epoxy paint for external platform	5	20-Oct-26	25-Oct-26	21-Nov-26	25-Nov-26	3,734.16	0.00	0.00	0%	0%
ARCHITECTURAL		88	26-Sep-26	19-Jan-27	30-Jul-26 A	07-Jan-27	900,244.66	52,504.85	97,556.91	5.83%	10.84%
MASONARY WORKS		21	26-Sep-26	27-Oct-26	06-Aug-26 A	06-Sep-26 A	78,954.21	52,504.85	78,954.21	66.5%	100%
DAM3-C-B11-A-0120	Block work at factory area	5	26-Sep-26	06-Oct-26	06-Aug-26 A	11-Aug-26 A	58,338.72	52,504.85	58,338.72	90%	100%
DAM3-C-B11-A-0150	Block work at office area	3	12-Oct-26	19-Oct-26	10-Aug-26 A	06-Sep-26 A	6,179.18	0.00	6,179.18	0%	100%
DAM3-C-B11-A-170	Block work at toilet area	4	20-Oct-26	27-Oct-26	13-Aug-26 A	06-Sep-26 A	14,436.31	0.00	14,436.31	0%	100%
WALL FINISHES		23	07-Nov-26	22-Dec-26	27-Sep-26 A	22-Dec-26	92,757.47	0.00	12,147.54	0%	13.1%
DAM3-C-B11-A-180	Internal Wall Plaster	10	07-Nov-26	23-Nov-26	27-Sep-26 A	05-Dec-26	48,590.16	0.00	12,147.54	0%	25%
DAM3-C-B11-A-230	Paint to Plaster (Primer, Putty & First Coat)	4	15-Dec-26	22-Dec-26	17-Dec-26	22-Dec-26	44,167.30	0.00	0.00	0%	0%
CIELING FINISHES		5	07-Dec-26	12-Dec-26	15-Dec-26	21-Dec-26	46,792.30	0.00	0.00	0%	0%
DAM3-C-B11-A-240	Installation of Ceiling Gypsum Board	5	07-Dec-26	12-Dec-26	15-Dec-26	21-Dec-26	46,792.30	0.00	0.00	0%	0%
FLOOR FINISHES		17	29-Nov-26	19-Jan-27	09-Dec-26	29-Dec-26	189,488.90	0.00	0.00	0%	0%
DAM3-C-B11-A-220	Tiles for Toilet	5	29-Nov-26	06-Dec-26	09-Dec-26	15-Dec-26	46,530.71	0.00	0.00	0%	0%
DAM3-C-B11-A-250	Tiles for Office Area	2	13-Dec-26	14-Dec-26	15-Dec-26	17-Dec-26	26,867.31	0.00	0.00	0%	0%
DAM3-C-B11-A-390	Granite strip	2	15-Dec-26	16-Dec-26	17-Dec-26	20-Dec-26	671.12	0.00	0.00	0%	0%
DAM3-C-B11-A-420	Epoxy paint	7	12-Jan-27	19-Jan-27	21-Dec-26	29-Dec-26	115,419.76	0.00	0.00	0%	0%
DOORS & WINDOWS		14	26-Oct-26	10-Nov-26	12-Nov-26	28-Nov-26	248,575.06	0.00	0.00	0%	0%
DAM3-C-B11-A-552	Window (CW1)	7	26-Oct-26	02-Nov-26	12-Nov-26	19-Nov-26	94,173.21	0.00	0.00	0%	0%
DAM3-C-B11-A-553	Roll up Shutter Door	1	03-Nov-26	03-Nov-26	21-Nov-26	21-Nov-26	68,619.20	0.00	0.00	0%	0%
DAM3-C-B11-A-200	Supply and install (D5) 1000*2200mm single leaf steel door with door	1	04-Nov-26	04-Nov-26	22-Nov-26	22-Nov-26	16,016.16	0.00	0.00	0%	0%
DAM3-C-B11-A-554	Supply and install (D4) 800*2200 mm single leaf aluminum door with door	1	05-Nov-26	05-Nov-26	23-Nov-26	23-Nov-26	22,737.85	0.00	0.00	0%	0%
DAM3-C-B11-A-555	Supply and install (D7) 1000*2200 mm single leaf aluminum door with door	1	07-Nov-26	07-Nov-26	24-Nov-26	24-Nov-26	7,811.07	0.00	0.00	0%	0%
DAM3-C-B11-A-556	Supply and install (D3) 1000*2200 mm single leaf aluminum door with door	1	08-Nov-26	08-Nov-26	25-Nov-26	25-Nov-26	16,016.16	0.00	0.00	0%	0%
DAM3-C-B11-A-557	Supply and install fire rated 45 min (D2) 1200*2200 mm single leaf steel doo	1	09-Nov-26	09-Nov-26	26-Nov-26	26-Nov-26	16,711.52	0.00	0.00	0%	0%
DAM3-C-B11-A-558	Skylight fixtures installation	1	10-Nov-26	10-Nov-26	28-Nov-26	28-Nov-26	6,489.89	0.00	0.00	0%	0%
WATER PROOFING WORKS		4	24-Nov-26	28-Nov-26	05-Dec-26	09-Dec-26	4,879.02	0.00	0.00	0%	0%
DAM3-C-B11-A-370	Waterproofing membrane for toilets	4	24-Nov-26	28-Nov-26	05-Dec-26	09-Dec-26	4,879.02	0.00	0.00	0%	0%
METAL WORKS		56	17-Dec-26	31-Dec-26	30-Jul-26 A	30-Dec-26	193,717.06	0.00	6,455.16	0%	3.33%
DAM3-C-B11-A-300	Galvanised Steel Gratings	2	30-Dec-26	31-Dec-26	30-Jul-26 A	30-Jul-26 A	6,455.16	0.00	6,455.16	0%	100%
DAM3-C-B11-A-290	Steel Ladder	2	17-Dec-26	19-Dec-26	20-Dec-26	22-Dec-26	9,839.16	0.00	0.00	0%	0%
DAM3-C-B11-A-291	Steel railing works	4	20-Dec-26	23-Dec-26	22-Dec-26	27-Dec-26	1,533.98	0.00	0.00	0%	0%
DAM3-C-B11-A-292	Aluminium composite panel	3	24-Dec-26	29-Dec-26	27-Dec-26	30-Dec-26	175,888.76	0.00	0.00	0%	0%
SPECIALTIES		7	02-Jan-27	11-Jan-27	30-Dec-26	07-Jan-27	45,080.66	0.00	0.00	0%	0%
DAM3-C-B11-A-320	Installation of fittings	3	02-Jan-27	06-Jan-27	30-Dec-26	03-Jan-27	22,981.27	0.00	0.00	0%	0%
DAM3-C-B11-A-570	Identification sign; ID01 & ID02	3	07-Jan-27	10-Jan-27	03-Jan-27	06-Jan-27	9,630.56	0.00	0.00	0%	0%
DAM3-C-B11-A-340	Furniture Installation	1	11-Jan-27	11-Jan-27	06-Jan-27	07-Jan-27	12,468.83	0.00	0.00	0%	0%
MECHANICAL		182	19-May-26	11-Jan-27	05-Jul-26 A	10-Jan-27	467,522.66	18,585.14	114,688.10	3.98%	24.53%
HVAC		13	23-Dec-26	07-Jan-27	22-Dec-26	06-Jan-27	233,183.33	0.00	0.00	0%	0%

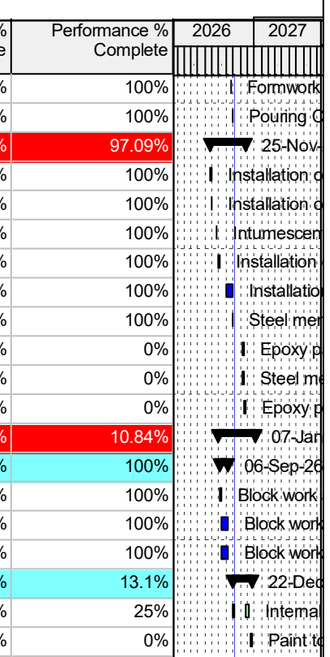


Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary

Date	Revision	Checked	Approved
06-Oct-26	Weekly Report		

Activity ID	Activity Name	Original Duration	BL Project Start	BL Project Finish	Start	Finish	Budgeted Total Cost	Planned Value Cost	Earned Value Cost	Schedule % Complete	Performance % Complete
FIRST STAGE		4	30-Dec-26	03-Jan-27	28-Dec-26	02-Jan-27	170,694.73	0.00	0.00	0%	0%
DAM3-C-B11-M-140	Installation of HVAC Ducts	2	30-Dec-26	31-Dec-26	28-Dec-26	30-Dec-26	149,489.33	0.00	0.00	0%	0%
DAM3-C-B11-M-170	Installation of Duct insulation	2	02-Jan-27	03-Jan-27	30-Dec-26	02-Jan-27	21,205.40	0.00	0.00	0%	0%
SECOND STAGE		13	23-Dec-26	07-Jan-27	22-Dec-26	06-Jan-27	62,488.60	0.00	0.00	0%	0%
DAM3-C-B11-M-130	Installation of Exhaust Fans	2	23-Dec-26	24-Dec-26	22-Dec-26	24-Dec-26	7,938.56	0.00	0.00	0%	0%
DAM3-C-B11-M-160	Installation of Wall Propeller Type Exhaust Fan	3	26-Dec-26	29-Dec-26	24-Dec-26	28-Dec-26	46,831.64	0.00	0.00	0%	0%
DAM3-C-B11-M-339	Installation of Diffuser	2	04-Jan-27	05-Jan-27	02-Jan-27	04-Jan-27	2,144.00	0.00	0.00	0%	0%
DAM3-C-B11-M-340	Supply, install, test and commission door grilles & exhaust louvers	2	06-Jan-27	07-Jan-27	04-Jan-27	06-Jan-27	5,574.40	0.00	0.00	0%	0%
FIRE FIGHTING SYSTEM		16	23-Dec-26	11-Jan-27	29-Aug-26 A	10-Jan-27	102,458.78	0.00	84,594.16	0%	82.56%
FIRST STAGE		8	23-Dec-26	05-Jan-27	29-Aug-26 A	07-Sep-26 A	84,594.16	0.00	84,594.16	0%	100%
DAM3-C-B11-M-300	Installation of Fire Fighting Pipes (Seamless Black Steel)	5	23-Dec-26	30-Dec-26	29-Aug-26 A	05-Sep-26 A	72,394.75	0.00	72,394.75	0%	100%
DAM3-C-B11-M-310	Installation of Fire Fighting Valve	3	31-Dec-26	05-Jan-27	30-Aug-26 A	07-Sep-26 A	12,199.40	0.00	12,199.40	0%	100%
SECOND STAGE		16	06-Jan-27	11-Jan-27	22-Dec-26	10-Jan-27	17,864.62	0.00	0.00	0%	0%
DAM3-C-B11-M-320	Installation of Fire Hose Cabinet	3	06-Jan-27	09-Jan-27	22-Dec-26	26-Dec-26	15,158.56	0.00	0.00	0%	0%
DAM3-C-B11-M-370	Supply, install, test and commission Fire Department Connection(FDC)	3	09-Jan-27	11-Jan-27	06-Jan-27	10-Jan-27	2,706.06	0.00	0.00	0%	0%
SEWER AND DRAINAGE SYSTEM		182	19-May-26	30-Dec-26	05-Jul-26 A	03-Jan-27	90,009.74	18,585.14	30,093.94	20.65%	33.43%
FIRST STAGE		182	19-May-26	14-Dec-26	05-Jul-26 A	17-Dec-26	41,149.90	18,585.14	30,093.94	45.16%	73.13%
DAM3-C-B11-M-200	Installation of Sanitary Waste / Drainage Pipes	4	19-May-26	23-May-26	05-Jul-26 A	08-Jul-26 A	18,585.14	18,585.14	18,585.14	100%	100%
DAM3-C-B11-M-380	Installation of Trench drain	5	09-Dec-26	14-Dec-26	06-Jul-26 A	08-Jul-26 A	11,508.80	0.00	11,508.80	0%	100%
DAM3-C-B11-M-220	Installation of Floor Drain	2	07-Dec-26	08-Dec-26	15-Dec-26	17-Dec-26	11,055.96	0.00	0.00	0%	0%
SECOND STAGE		14	15-Dec-26	30-Dec-26	17-Dec-26	03-Jan-27	48,859.84	0.00	0.00	0%	0%
DAM3-C-B11-M-180	Installation of Electric Water Heater	2	15-Dec-26	16-Dec-26	17-Dec-26	20-Dec-26	1,819.51	0.00	0.00	0%	0%
DAM3-C-B11-M-190	Installation of Sanitary Fixture and Accessories	4	17-Dec-26	21-Dec-26	20-Dec-26	24-Dec-26	19,921.72	0.00	0.00	0%	0%
DAM3-C-B11-M-210	Installation of Lavotary /Wash Basin	2	22-Dec-26	23-Dec-26	24-Dec-26	27-Dec-26	21,416.68	0.00	0.00	0%	0%
DAM3-C-B11-M-270	Installation of Bib Tap	2	24-Dec-26	26-Dec-26	27-Dec-26	29-Dec-26	1,900.66	0.00	0.00	0%	0%
DAM3-C-B11-M-428	Installation of Water Tap	2	27-Dec-26	28-Dec-26	29-Dec-26	31-Dec-26	2,874.14	0.00	0.00	0%	0%
DAM3-C-B11-M-429	Installation of Roof Vent Cap	2	29-Dec-26	30-Dec-26	31-Dec-26	03-Jan-27	927.12	0.00	0.00	0%	0%
WATER SUPPLY SYSTEM		11	23-Dec-26	04-Jan-27	22-Dec-26	04-Jan-27	41,870.81	0.00	0.00	0%	0%
FIRST STAGE		6	23-Dec-26	29-Dec-26	22-Dec-26	29-Dec-26	41,592.68	0.00	0.00	0%	0%
DAM3-C-B11-M-290	Installation of Water Supply Pipes	4	23-Dec-26	27-Dec-26	22-Dec-26	27-Dec-26	23,318.41	0.00	0.00	0%	0%
DAM3-C-B11-M-280	Installation of Water Supply Valve	2	28-Dec-26	29-Dec-26	27-Dec-26	29-Dec-26	18,274.27	0.00	0.00	0%	0%
SECOND STAGE		5	30-Dec-26	04-Jan-27	29-Dec-26	04-Jan-27	278.13	0.00	0.00	0%	0%
DAM3-C-B11-M-330	Capped connection	5	30-Dec-26	04-Jan-27	29-Dec-26	04-Jan-27	278.13	0.00	0.00	0%	0%
ELECTRICAL		87	28-Oct-26	16-Feb-27	01-Jun-26 A	24-Feb-27	752,044.76	0.00	20,026.20	0%	2.66%
FIRST STAGE		79	28-Oct-26	09-Dec-26	01-Jun-26 A	22-Dec-26	86,114.12	0.00	20,026.20	0%	23.26%
DAM3-C-B11-E-113	Installation of Earthing and Grounding	3	05-Dec-26	09-Dec-26	01-Jun-26 A	22-Dec-26	19,646.47	0.00	17,681.82	0%	90%
DAM3-C-B11-E-143	Installation of Conduits and wiring outlets - Fire Alarm System	4	28-Oct-26	01-Nov-26	02-Jun-26 A	18-Nov-26	1,768.31	0.00	884.15	0%	50%
DAM3-C-B11-E-183	Installation of Sleeves & Power outlet	8	28-Oct-26	05-Nov-26	02-Jun-26 A	21-Nov-26	2,920.45	0.00	1,460.23	0%	50%
DAM3-C-B11-E-163	Installation of Conduites for Lighting Fixture	4	11-Nov-26	15-Nov-26	29-Nov-26	02-Dec-26	8,462.97	0.00	0.00	0%	0%
DAM3-C-B11-E-233	Installation of Wires	4	16-Nov-26	19-Nov-26	03-Dec-26	07-Dec-26	16,925.94	0.00	0.00	0%	0%
DAM3-C-B11-E-223	Installation of LV Cables	4	30-Nov-26	03-Dec-26	17-Dec-26	21-Dec-26	36,389.98	0.00	0.00	0%	0%
SECOND STAGE		83	02-Nov-26	16-Feb-27	19-Nov-26	24-Feb-27	665,930.64	0.00	0.00	0%	0%
DAM3-C-B11-E-123	Installation of Fire Alarm Control Panel	4	02-Nov-26	05-Nov-26	19-Nov-26	23-Nov-26	19,451.37	0.00	0.00	0%	0%
DAM3-C-B11-E-133	Installation of Fire Detectors & Accessories	4	07-Nov-26	10-Nov-26	24-Nov-26	28-Nov-26	56,740.37	0.00	0.00	0%	0%
DAM3-C-B11-E-153	Installation of Lighting fixtures	4	21-Nov-26	24-Nov-26	08-Dec-26	12-Dec-26	76,166.74	0.00	0.00	0%	0%
DAM3-C-B11-E-193	Installation of Main Distribution Board	2	21-Nov-26	22-Nov-26	08-Dec-26	09-Dec-26	32,472.73	0.00	0.00	0%	0%
DAM3-C-B11-E-410	Installation of CCTV System	5	21-Nov-26	28-Nov-26	08-Dec-26	13-Dec-26	76,349.24	0.00	0.00	0%	0%
DAM3-C-B11-E-243	Installation of LP-1 Panel	2	23-Nov-26	24-Nov-26	10-Dec-26	12-Dec-26	18,403.54	0.00	0.00	0%	0%
DAM3-C-B11-E-253	Installation of PP-AC panel	2	25-Nov-26	26-Nov-26	13-Dec-26	14-Dec-26	21,648.48	0.00	0.00	0%	0%

Activity ID	Activity Name	Original Duration	BL Project Start	BL Project Finish	Start	Finish	Budgeted Total Cost	Planned Value Cost	Earned Value Cost	Schedule % Complete	Performance % Complete
DAM3-C-B11-E-273	Installation of Access Control System	5	29-Nov-26	03-Dec-26	14-Dec-26	19-Dec-26	27,616.86	0.00	0.00	0%	0%
DAM3-C-B11-E-213	Installation of Telephone Cabinet	2	28-Nov-26	29-Nov-26	15-Dec-26	16-Dec-26	26,991.08	0.00	0.00	0%	0%
DAM3-C-B11-E-283	Monitor Modules for Fire Alarm	2	05-Dec-26	06-Dec-26	20-Dec-26	21-Dec-26	3,882.38	0.00	0.00	0%	0%
DAM3-C-B11-E-293	Line Isolator Modules for Fire Alarm	2	07-Dec-26	08-Dec-26	22-Dec-26	23-Dec-26	185.40	0.00	0.00	0%	0%
DAM3-C-B11-E-173	Installation of Wiring Devices	4	23-Dec-26	27-Dec-26	22-Dec-26	27-Dec-26	19,435.09	0.00	0.00	0%	0%
DAM3-C-B11-E-303	Firewarning flash light with sounder; wall mounted, Weather proof	2	09-Dec-26	10-Dec-26	24-Dec-26	26-Dec-26	3,082.69	0.00	0.00	0%	0%
DAM3-C-B11-E-203	Installation of Disconnect Switches	2	28-Dec-26	29-Dec-26	27-Dec-26	29-Dec-26	30,235.95	0.00	0.00	0%	0%
DAM3-C-B11-E-420	Installation of Solar power plant	4	09-Feb-27	16-Feb-27	18-Feb-27	24-Feb-27	253,268.71	0.00	0.00	0%	0%
SITE INFRASTRUCTURE		290	10-Feb-26	21-Feb-27	19-Jan-26 A	27-Feb-27	8,476,025.35	1,639,837.85	2,533,555.40	19.35%	29.89%
SITE WORKS		23	10-Feb-26	10-Mar-26	19-Jan-26 A	28-Feb-26 A	197,690.88	197,690.88	197,690.88	100%	100%
DAM3-C-GEN-180	Initial Site Survey and Setting out	3	10-Feb-26	12-Feb-26	19-Jan-26 A	24-Jan-26 A	0.00	0.00	0.00	100%	100%
DAM3-C-GEN-190	Excavation to the target grading level	20	14-Feb-26	10-Mar-26	10-Feb-26 A	28-Feb-26 A	197,690.88	197,690.88	197,690.88	100%	100%
NETWORKS		90	07-Sep-26	23-Dec-26	01-Aug-26 A	01-Feb-27	1,901,944.63	670,749.27	1,180,962.82	35.27%	62.09%
INTERNAL FIRE FIGHTING WATER SUPPLY SYSTEM (OUTSIDE BUILDING UNITS)		42	07-Sep-26	21-Oct-26	01-Aug-26 A	25-Nov-26	571,716.96	531,245.38	497,845.16	92.92%	87.08%
DAM3-C-ENV-F-212	Excavation for External Fire Fighting Works	7	07-Sep-26	14-Sep-26	01-Aug-26 A	12-Nov-26	40,471.58	40,471.58	36,424.43	100%	90%
DAM3-C-ENV-F-172	Installation of HDPE PN16 Pipes (200 Dia)	10	15-Sep-26	27-Sep-26	02-Aug-26 A	14-Nov-26	364,244.28	364,244.28	327,819.85	100%	90%
DAM3-C-ENV-F-192	Installation of Valves	5	30-Sep-26	05-Oct-26	02-Aug-26 A	22-Nov-26	86,057.93	86,057.93	68,846.34	100%	80%
DAM3-C-ENV-F-202	Warning Tapes	2	28-Sep-26	29-Sep-26	03-Aug-26 A	21-Nov-26	40,471.58	40,471.58	32,377.27	100%	80%
DAM3-C-ENV-F-222	Backfilling for External Fire Fighting Works	14	06-Oct-26	21-Oct-26	05-Aug-26 A	25-Nov-26	40,471.58	0.00	32,377.27	0%	80%
WATER SUPPLY SYSTEM		56	15-Sep-26	23-Dec-26	22-Nov-26	25-Jan-27	290,579.64	139,503.89	0.00	48.01%	0%
DAM3-C-ENV-WS-786	Excavation for Water Suppy Works	7	15-Sep-26	22-Sep-26	22-Nov-26	29-Nov-26	13,950.39	13,950.39	0.00	100%	0%
DAM3-C-ENV-WS-746	Installation of HDPE PN16 Pipes for Cold Water Supply	7	24-Sep-26	05-Oct-26	30-Nov-26	07-Dec-26	125,553.50	125,553.50	0.00	100%	0%
DAM3-C-ENV-WS-806	Construction of Washout Chamber	7	06-Oct-26	13-Oct-26	08-Dec-26	15-Dec-26	17,314.15	0.00	0.00	0%	0%
DAM3-C-ENV-WS-776	Warning Tape	2	14-Oct-26	15-Oct-26	16-Dec-26	17-Dec-26	13,950.39	0.00	0.00	0%	0%
DAM3-C-ENV-WS-846	Construction of Air Valve Chamber	7	14-Oct-26	21-Oct-26	16-Dec-26	23-Dec-26	16,236.37	0.00	0.00	0%	0%
DAM3-C-ENV-WS-766	Installation of Valves	5	16-Nov-26	21-Nov-26	19-Dec-26	23-Dec-26	53,930.05	0.00	0.00	0%	0%
DAM3-C-ENV-WS-796	Backfilling for Water Supply	14	22-Nov-26	07-Dec-26	24-Dec-26	09-Jan-27	13,950.39	0.00	0.00	0%	0%
DAM3-C-ENV-WS-826	Supply and install Service connection -HDPE	14	08-Dec-26	23-Dec-26	10-Jan-27	25-Jan-27	35,694.38	0.00	0.00	0%	0%
SEWER & DRAINAGE SYSTEM		36	06-Oct-26	08-Dec-26	22-Aug-26 A	27-Dec-26	772,226.27	0.00	683,117.66	0%	88.46%
DAM3-C-ENV-SW-496	Construction of inspection chambers	7	03-Nov-26	10-Nov-26	22-Aug-26 A	03-Oct-26 A	249,925.25	0.00	249,925.25	0%	100%
DAM3-C-ENV-SW-516	Excavation for Sewer Works	7	06-Oct-26	13-Oct-26	22-Aug-26 A	04-Oct-26 A	22,261.94	0.00	22,261.94	0%	100%
DAM3-C-ENV-SW-536	Construction of Manhole	7	26-Oct-26	02-Nov-26	22-Aug-26 A	10-Sep-26 A	166,049.07	0.00	166,049.07	0%	100%
DAM3-C-ENV-SW-486	Installation of UPVC Pipes for Sewer	4	14-Oct-26	25-Oct-26	16-Sep-26 A	05-Oct-26 A	222,619.45	0.00	222,619.45	0%	100%
DAM3-C-ENV-SW-526	Backfilling for Sewer Drainage	14	03-Nov-26	18-Nov-26	17-Sep-26 A	06-Oct-26 A	22,261.94	0.00	22,261.94	0%	100%
DAM3-C-ENV-SW-506	Gully trap	10	19-Nov-26	30-Nov-26	08-Dec-26	19-Dec-26	53,541.58	0.00	0.00	0%	0%
DAM3-C-ENV-SW-546	UPVC pipe service connection	7	01-Dec-26	08-Dec-26	20-Dec-26	27-Dec-26	35,567.03	0.00	0.00	0%	0%
IRRIGATION SYSTEM		48	06-Oct-26	22-Dec-26	08-Dec-26	01-Feb-27	267,421.77	0.00	0.00	0%	0%
DAM3-C-ENV-SW-556	Excavation for HDPE pipes	7	06-Oct-26	13-Oct-26	08-Dec-26	15-Dec-26	6,309.39	0.00	0.00	0%	0%
DAM3-C-ENV-SW-566	Installation of HDPE Pipes	10	14-Oct-26	25-Oct-26	16-Dec-26	27-Dec-26	63,093.94	0.00	0.00	0%	0%
DAM3-C-ENV-SW-586	Construction of Washout valve chamber	5	26-Oct-26	31-Oct-26	28-Dec-26	02-Jan-27	3,247.85	0.00	0.00	0%	0%
DAM3-C-ENV-SW-576	Construction of Air valve chamber	5	26-Oct-26	31-Oct-26	28-Dec-26	02-Jan-27	3,786.75	0.00	0.00	0%	0%
DAM3-C-ENV-SW-596	Backfilling for HDPE pipes	14	01-Nov-26	16-Nov-26	03-Jan-27	18-Jan-27	6,309.39	0.00	0.00	0%	0%
DAM3-C-ENV-SW-606	Installation of valves	5	09-Dec-26	14-Dec-26	19-Jan-27	24-Jan-27	84,556.00	0.00	0.00	0%	0%
DAM3-C-ENV-SW-616	Main program system and controller for irrigation system	7	15-Dec-26	22-Dec-26	25-Jan-27	01-Feb-27	100,118.45	0.00	0.00	0%	0%
EXTERNAL WORKS		83	15-Sep-26	25-Jan-27	01-Jul-26 A	27-Feb-27	3,338,525.71	771,397.70	1,154,901.70	23.11%	34.59%
MECHANICAL		34	26-Oct-26	10-Jan-27	01-Jul-26 A	27-Dec-26	1,375,655.38	0.00	1,154,901.70	0%	83.95%
DAM3-C-ENV-M-1371	Installation of GRP Tanks	10	30-Nov-26	10-Dec-26	08-Aug-26 A	08-Dec-26	585,839.88	0.00	527,255.89	0%	90%
DAM3-C-ENV-M-1301	Installation of Fire Fighting Pump	4	31-Dec-26	04-Jan-27	22-Sep-26 A	22-Sep-26 A	345,880.31	0.00	345,880.31	0%	100%
DAM3-C-ENV-M-1341	Installation of Booster Pump	5	26-Dec-26	30-Dec-26	08-Dec-26	13-Dec-26	38,967.27	0.00	0.00	0%	0%

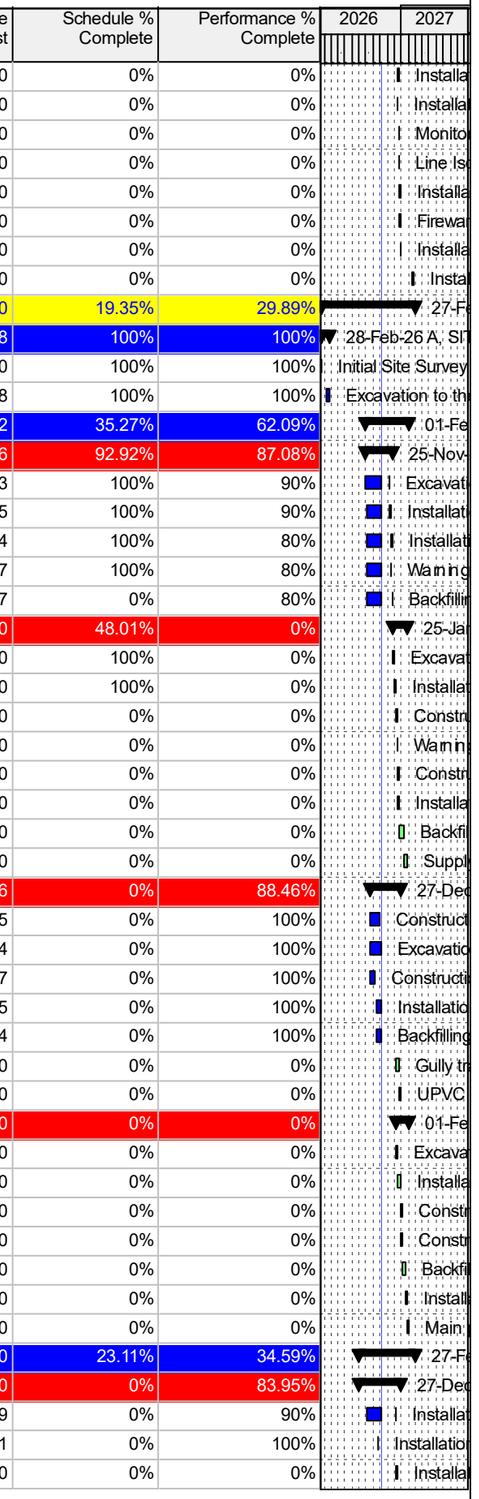

Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary

Date	Revision	Checked	Approved
06-Oct-26	Weekly Report		

Activity ID	Activity Name	Original Duration	BL Project Start	BL Project Finish	Start	Finish	Budgeted Total Cost	Planned Value Cost	Earned Value Cost	Schedule % Complete	Performance % Complete
DAM3-C-ENV-M-1311	CO2 fire extinguisher	1	05-Jan-27	05-Jan-27	14-Dec-26	14-Dec-26	217.29	0.00	0.00	0%	0%
DAM3-C-ENV-M-1361	Powder fire extinguisher	1	06-Jan-27	06-Jan-27	15-Dec-26	15-Dec-26	188.33	0.00	0.00	0%	0%
DAM3-C-ENV-M-1351	Valves for Water Supply Pump	2	03-Jan-27	04-Jan-27	16-Dec-26	17-Dec-26	4,329.70	0.00	0.00	0%	0%
DAM3-C-ENV-M-1381	Valves for GRP Tank	3	12-Dec-26	14-Dec-26	22-Dec-26	24-Dec-26	58,583.98	0.00	0.00	0%	0%
DAM3-C-ENV-M-1391	Access Ladder for GRP Tank	2	15-Dec-26	16-Dec-26	26-Dec-26	27-Dec-26	58,583.98	0.00	0.00	0%	0%
GRP Tank Foundation		31	31-Oct-26	29-Nov-26	27-Jul-26 A	27-Aug-26 A	180,037.46	0.00	180,037.46	0%	100%
DAM3-C-GRP-S-0101	Excavation for Foundation	4	31-Oct-26	03-Nov-26	27-Jul-26 A	27-Jul-26 A	9,001.87	0.00	9,001.87	0%	100%
DAM3-C-GRP-S-0103	Lean Concrete Below Foundation	2	07-Nov-26	08-Nov-26	06-Aug-26 A	06-Aug-26 A	18,003.75	0.00	18,003.75	0%	100%
DAM3-C-GRP-S-0102	Vapour Barrier for Foundation	2	04-Nov-26	05-Nov-26	06-Aug-26 A	06-Aug-26 A	9,001.87	0.00	9,001.87	0%	100%
DAM3-C-GRP-S-0104	Rebar for Foundation	4	09-Nov-26	12-Nov-26	11-Aug-26 A	16-Aug-26 A	36,007.49	0.00	36,007.49	0%	100%
DAM3-C-GRP-S-0105	Formwork for Foundation	4	14-Nov-26	17-Nov-26	12-Aug-26 A	23-Aug-26 A	18,003.75	0.00	18,003.75	0%	100%
DAM3-C-GRP-S-0106	Pouring Concrete for Foundation	1	18-Nov-26	18-Nov-26	18-Aug-26 A	23-Aug-26 A	63,013.11	0.00	63,013.11	0%	100%
DAM3-C-GRP-S-0107	Damp proof /Bitumin paint on Foundation	2	19-Nov-26	21-Nov-26	24-Aug-26 A	25-Aug-26 A	9,001.87	0.00	9,001.87	0%	100%
DAM3-C-GRP-S-0108	Backfilling / Compaction Around Foundation	7	22-Nov-26	29-Nov-26	26-Aug-26 A	27-Aug-26 A	18,003.75	0.00	18,003.75	0%	100%
Pump Shed		34	26-Oct-26	10-Jan-27	01-Jul-26 A	13-Dec-26	103,027.17	0.00	101,728.03	0%	98.74%
DAM3-C-PR-S-108	Excavation for Footings	4	26-Oct-26	29-Oct-26	01-Jul-26 A	02-Jul-26 A	649.57	0.00	649.57	0%	100%
DAM3-C-PR-S-138	Lean Concrete Below Footings	2	02-Nov-26	03-Nov-26	23-Jul-26 A	23-Jul-26 A	649.57	0.00	649.57	0%	100%
DAM3-C-PR-S-308	Vapour Barrier for Footings	2	31-Oct-26	01-Nov-26	23-Jul-26 A	23-Jul-26 A	649.57	0.00	649.57	0%	100%
DAM3-C-PR-S-198	Rebar for Footings	4	04-Nov-26	08-Nov-26	25-Jul-26 A	25-Jul-26 A	1,299.14	0.00	1,299.14	0%	100%
DAM3-C-PR-S-208	Formwork for Footings	4	09-Nov-26	12-Nov-26	25-Jul-26 A	25-Jul-26 A	649.57	0.00	649.57	0%	100%
DAM3-C-PR-S-148	Pouring Concrete for Footings	1	14-Nov-26	14-Nov-26	26-Jul-26 A	26-Jul-26 A	5,846.13	0.00	5,846.13	0%	100%
DAM3-C-PR-S-298	Damp proof /Bitumin paint on Footing Sides	2	15-Nov-26	16-Nov-26	28-Jul-26 A	28-Jul-26 A	649.57	0.00	649.57	0%	100%
DAM3-C-PR-S-378	Backfilling / Compaction Around Footings to Bottom of Grade Beams	5	17-Nov-26	22-Nov-26	29-Jul-26 A	03-Aug-26 A	1,299.14	0.00	1,299.14	0%	100%
DAM3-C-PR-S-158	Lean Concrete Below Grade Beams	2	25-Nov-26	26-Nov-26	04-Aug-26 A	04-Aug-26 A	649.57	0.00	649.57	0%	100%
DAM3-C-PR-S-328	Vapour barrier for Grade Beams	2	23-Nov-26	24-Nov-26	04-Aug-26 A	04-Aug-26 A	649.57	0.00	649.57	0%	100%
DAM3-C-PR-S-218	Rebar for Grade Beams	2	28-Nov-26	29-Nov-26	15-Aug-26 A	15-Aug-26 A	1,299.14	0.00	1,299.14	0%	100%
DAM3-C-PR-S-228	Formwork for Grade Beams	2	30-Nov-26	01-Dec-26	16-Aug-26 A	17-Aug-26 A	649.57	0.00	649.57	0%	100%
DAM3-C-PR-S-188	Pedestal including anchor bolts	1	30-Nov-26	30-Nov-26	17-Aug-26 A	17-Aug-26 A	1,299.14	0.00	1,299.14	0%	100%
DAM3-C-PR-S-168	Pouring Concrete for Grade Beams	1	02-Dec-26	02-Dec-26	18-Aug-26 A	18-Aug-26 A	3,247.85	0.00	3,247.85	0%	100%
DAM3-C-PR-S-338	Damp proof /Bitumin paint on Grade Beams	2	03-Dec-26	05-Dec-26	20-Aug-26 A	22-Aug-26 A	649.57	0.00	649.57	0%	100%
DAM3-C-PR-S-388	Backfilling / Compaction for Slab on Grade	5	06-Dec-26	10-Dec-26	23-Aug-26 A	24-Aug-26 A	1,299.14	0.00	1,299.14	0%	100%
DAM3-C-PR-S-318	Anti Termite Treatment below Ground Slab	1	12-Dec-26	12-Dec-26	24-Aug-26 A	24-Aug-26 A	649.57	0.00	649.57	0%	100%
DAM3-C-PR-S-348	Vapour barrier for below Ground Slab	2	13-Dec-26	14-Dec-26	24-Aug-26 A	24-Aug-26 A	649.57	0.00	649.57	0%	100%
DAM3-C-PR-S-268	Rebar for Ground Slab	4	15-Dec-26	19-Dec-26	25-Aug-26 A	26-Aug-26 A	12,070.63	0.00	12,070.63	0%	100%
DAM3-C-PR-S-278	Formwork for Ground Slab	4	20-Dec-26	23-Dec-26	26-Aug-26 A	26-Aug-26 A	8,263.60	0.00	8,263.60	0%	100%
DAM3-C-PR-S-178	Pouring Concrete for Ground Slab	1	24-Dec-26	24-Dec-26	27-Aug-26 A	27-Aug-26 A	20,334.24	0.00	20,334.24	0%	100%
DAM3-C-PR-S-128	Installation of Columns	3	31-Dec-26	03-Jan-27	30-Aug-26 A	30-Aug-26 A	7,794.85	0.00	7,794.85	0%	100%
DAM3-C-PR-S-358	Installation of Raft & Purlins	4	04-Jan-27	07-Jan-27	30-Aug-26 A	30-Aug-26 A	11,042.69	0.00	11,042.69	0%	100%
DAM3-C-PR-S-368	Installation of Roof Sheet	2	09-Jan-27	10-Jan-27	31-Aug-26 A	31-Aug-26 A	19,487.12	0.00	19,487.12	0%	100%
DAM3-C-PR-S-288	Concrete Pad	5	26-Dec-26	30-Dec-26	08-Dec-26	13-Dec-26	1,299.14	0.00	0.00	0%	0%
ELECTRICAL		17	31-Dec-26	25-Jan-27	14-Dec-26	02-Jan-27	236,867.32	0.00	0.00	0%	0%
DAM3-C-ENV-E-176	Installation of Main MCC	2	31-Dec-26	02-Jan-27	14-Dec-26	15-Dec-26	13,498.43	0.00	0.00	0%	0%
DAM3-C-ENV-E-236	Installation of panel boards	2	05-Jan-27	06-Jan-27	14-Dec-26	15-Dec-26	5,953.91	0.00	0.00	0%	0%
DAM3-C-ENV-E-1321	Installation of wiring devices	5	07-Jan-27	12-Jan-27	16-Dec-26	21-Dec-26	5,632.31	0.00	0.00	0%	0%
DAM3-C-ENV-E-186	Installation of Earthing and Grounding	3	03-Jan-27	07-Jan-27	16-Dec-26	19-Dec-26	1,399.38	0.00	0.00	0%	0%
DAM3-C-ENV-E-1341	Installation of Cable tray	5	07-Jan-27	12-Jan-27	16-Dec-26	21-Dec-26	3,563.73	0.00	0.00	0%	0%
DAM3-C-ENV-E-206	Installation of Conduites for Lighting Fixture	4	09-Jan-27	12-Jan-27	20-Dec-26	23-Dec-26	798.20	0.00	0.00	0%	0%
DAM3-C-ENV-E-216	Installation of LV Cables	5	13-Jan-27	18-Jan-27	22-Dec-26	27-Dec-26	7,709.71	0.00	0.00	0%	0%
DAM3-C-ENV-E-226	Installation of Wires	2	13-Jan-27	14-Jan-27	24-Dec-26	26-Dec-26	1,596.40	0.00	0.00	0%	0%

Activity ID	Activity Name	Original Duration	BL Project Start	BL Project Finish	Start	Finish	Budgeted Total Cost	Planned Value Cost	Earned Value Cost	Schedule % Complete	Performance % Complete	2026	2027
DAM3-C-ENV-E-196	Installation of Lighting fixtures	2	16-Jan-27	17-Jan-27	27-Dec-26	28-Dec-26	7,183.81	0.00	0.00	0%	0%		Installa
DAM3-C-ENV-E-1331	Installation of Programmable Logis Controller	4	18-Jan-27	25-Jan-27	29-Dec-26	02-Jan-27	189,531.43	0.00	0.00	0%	0%		Installa
EXTERNAL ELECTRICAL WORKS		65	15-Sep-26	01-Dec-26	22-Nov-26	04-Feb-27	1,711,707.92	771,397.70	0.00	45.07%	0%		04-Fe
DAM3-C-ENV-E-400	Installation of UPVC Pipe	5	15-Sep-26	20-Sep-26	22-Nov-26	26-Nov-26	76,356.22	76,356.22	0.00	100%	0%		Installat
DAM3-C-ENV-E-410	Construction of Concrete encased duct bank	8	21-Sep-26	03-Oct-26	07-Dec-26	16-Dec-26	687,205.97	687,205.97	0.00	100%	0%		Constru
DAM3-C-ENV-E-420	Installation of Sleeves for lighting poles	5	04-Oct-26	08-Oct-26	16-Dec-26	22-Dec-26	19,588.78	7,835.51	0.00	40%	0%		Installa
DAM3-C-ENV-E-390	Installation of Telecom manhole	4	10-Oct-26	20-Oct-26	22-Dec-26	27-Dec-26	120,350.16	0.00	0.00	0%	0%		Installa
DAM3-C-ENV-E-450	Foundation for Lighting poles	5	21-Oct-26	26-Oct-26	27-Dec-26	02-Jan-27	19,588.78	0.00	0.00	0%	0%		Foundi
DAM3-C-ENV-E-440	Installation of Lighting poles	5	27-Oct-26	03-Nov-26	02-Jan-27	07-Jan-27	156,710.21	0.00	0.00	0%	0%		Installa
DAM3-C-ENV-E-430	Installation of Lighting Fixture	5	04-Nov-26	09-Nov-26	07-Jan-27	13-Jan-27	39,177.55	0.00	0.00	0%	0%		Installa
DAM3-C-ENV-E-380	Installation of LV Cables	7	10-Nov-26	17-Nov-26	13-Jan-27	21-Jan-27	98,914.91	0.00	0.00	0%	0%		Installa
DAM3-C-ENV-E-460	Electrical Manhole	7	18-Nov-26	25-Nov-26	21-Jan-27	30-Jan-27	253,329.40	0.00	0.00	0%	0%		Electri
DAM3-C-ENV-E-470	Installation of Earthing and Grounding	5	26-Nov-26	01-Dec-26	30-Jan-27	04-Feb-27	19,643.55	0.00	0.00	0%	0%		Install
DAM3-C-ENV-E-480	Installation of Street Lighting Feeder pillars & KWH meter	5	26-Nov-26	01-Dec-26	30-Jan-27	04-Feb-27	220,842.40	0.00	0.00	0%	0%		Install
FENCES AND GATES		37	10-Nov-26	10-Jan-27	13-Jan-27	27-Feb-27	14,295.10	0.00	0.00	0%	0%		27-Fe
DAM3-C-ENV-S-1374	Excavation for Fence	2	10-Nov-26	17-Nov-26	13-Jan-27	16-Jan-27	597.56	0.00	0.00	0%	0%		Excav
DAM3-C-ENV-S-1354	Vapour Barrier for Fence	4	18-Nov-26	22-Nov-26	16-Jan-27	20-Jan-27	298.78	0.00	0.00	0%	0%		Vapou
DAM3-C-ENV-S-1274	Lean Concrete Below Fence	4	23-Nov-26	26-Nov-26	20-Jan-27	25-Jan-27	597.56	0.00	0.00	0%	0%		Lean
DAM3-C-ENV-S-1304	Rebar for Footings	7	28-Nov-26	05-Dec-26	25-Jan-27	02-Feb-27	1,195.12	0.00	0.00	0%	0%		Rebar
DAM3-C-ENV-S-1314	Formwork for Footings	4	06-Dec-26	09-Dec-26	02-Feb-27	07-Feb-27	597.56	0.00	0.00	0%	0%		Formv
DAM3-C-ENV-S-1284	Pouring Concrete for Footings	2	10-Dec-26	12-Dec-26	07-Feb-27	09-Feb-27	1,792.67	0.00	0.00	0%	0%		Pourir
DAM3-C-ENV-S-1344	Damp proof /Bitumin paint on Footing Sides	2	13-Dec-26	14-Dec-26	09-Feb-27	11-Feb-27	298.78	0.00	0.00	0%	0%		Dampr
DAM3-C-ENV-S-1364	Backfilling / Compaction Around Footings	4	15-Dec-26	22-Dec-26	11-Feb-27	16-Feb-27	597.56	0.00	0.00	0%	0%		Backf
DAM3-C-ENV-S-1334	Installation of base plate	2	23-Dec-26	28-Dec-26	16-Feb-27	18-Feb-27	1,195.12	0.00	0.00	0%	0%		Instal
DAM3-C-ENV-S-1324	Installation of steel members	2	29-Dec-26	05-Jan-27	18-Feb-27	21-Feb-27	2,390.24	0.00	0.00	0%	0%		Instal
DAM3-C-ENV-S-1294	Installation of steel fence	2	06-Jan-27	07-Jan-27	21-Feb-27	24-Feb-27	2,390.24	0.00	0.00	0%	0%		Instal
DAM3-C-ENV-S-1384	Installation of steel gates	2	09-Jan-27	10-Jan-27	24-Feb-27	27-Feb-27	2,343.91	0.00	0.00	0%	0%		Instal
ROAD WORKS		34	23-Nov-26	21-Feb-27	16-Jan-27	25-Feb-27	2,873,764.57	0.00	0.00	0%	0%		25-Fe
DAM3-C-ENV-R-1390	SubGrade Preparation & Compaction	5	23-Nov-26	03-Dec-26	16-Jan-27	21-Jan-27	319,796.23	0.00	0.00	0%	0%		SubG
DAM3-C-ENV-R-1400	Aggregate Base Course Layer	5	05-Dec-26	12-Dec-26	21-Jan-27	27-Jan-27	262,382.32	0.00	0.00	0%	0%		Aggre
DAM3-C-ENV-R-1460	Curb Stones	4	13-Dec-26	04-Jan-27	27-Jan-27	01-Feb-27	291,156.54	0.00	0.00	0%	0%		Curb
DAM3-C-ENV-R-1480	Interlock Tiles	3	05-Jan-27	27-Jan-27	01-Feb-27	04-Feb-27	475,633.54	0.00	0.00	0%	0%		Interlo
DAM3-C-ENV-R-890	Supply and install geotextile sheet	2	28-Jan-27	30-Jan-27	04-Feb-27	07-Feb-27	47,639.01	0.00	0.00	0%	0%		Supp
DAM3-C-ENV-R-1490	Gravel Bedding	2	31-Jan-27	01-Feb-27	07-Feb-27	09-Feb-27	57,375.45	0.00	0.00	0%	0%		Grave
DAM3-C-ENV-R-1500	Road Signs	3	02-Feb-27	07-Feb-27	09-Feb-27	13-Feb-27	103,945.80	0.00	0.00	0%	0%		Road
DAM3-C-ENV-R-1450	Prime Coat	1	08-Feb-27	08-Feb-27	13-Feb-27	14-Feb-27	71,708.03	0.00	0.00	0%	0%		Prime
DAM3-C-ENV-R-1410	Asphalt Concrete Base Course Layer	2	09-Feb-27	10-Feb-27	14-Feb-27	16-Feb-27	645,372.33	0.00	0.00	0%	0%		Asphi
DAM3-C-ENV-R-1470	Tack Coat	1	11-Feb-27	11-Feb-27	16-Feb-27	17-Feb-27	52,885.08	0.00	0.00	0%	0%		Tack
DAM3-C-ENV-R-1420	Asphalt Concrete Wearing Course Layer	2	13-Feb-27	14-Feb-27	17-Feb-27	20-Feb-27	475,965.66	0.00	0.00	0%	0%		Asphi
DAM3-C-ENV-R-1430	Retroreflective Thermoplastic White Traffic lines	2	15-Feb-27	16-Feb-27	20-Feb-27	23-Feb-27	37,884.84	0.00	0.00	0%	0%		Retro
DAM3-C-ENV-R-1440	Installation of Concrete wheel bumper	2	17-Feb-27	21-Feb-27	23-Feb-27	25-Feb-27	32,019.76	0.00	0.00	0%	0%		Instal
LANDSCAPING		12	02-Feb-27	15-Feb-27	09-Feb-27	24-Feb-27	164,099.55	0.00	0.00	0%	0%		24-Fe
DAM3-C-ENV-R-1510	Planting of trees	5	02-Feb-27	07-Feb-27	09-Feb-27	15-Feb-27	110,131.54	0.00	0.00	0%	0%		Plant
DAM3-C-ENV-R-1520	Planting of shrubs	7	08-Feb-27	15-Feb-27	15-Feb-27	24-Feb-27	53,968.01	0.00	0.00	0%	0%		Plant
TESTING AND COMMISSIONING (10%)		185	24-May-26	18-Feb-27	17-Jun-26 A	27-Feb-27	9,599,652.50	7,188,932.37	7,173,095.73	74.89%	74.72%		27-Fe
TESTING AND COMMISSIONING 900 Sq.m-2		185	24-May-26	18-Feb-27	28-Jun-26 A	27-Feb-27	1,943,587.85	63,346.56	47,509.92	3.26%	2.44%		27-Fe
MECHANICAL		183	24-May-26	17-Jan-27	28-Jun-26 A	24-Feb-27	617,124.79	63,346.56	47,509.92	10.26%	7.7%		24-Fe
P001-C-TC-M-3406	Testing & Commissioning of Sewer & Drainage Pipes	7	24-May-26	03-Jun-26	28-Jun-26 A	07-Oct-26	63,346.56	63,346.56	47,509.92	100%	75%		Testing &
P001-C-TC-M-3416	Testing and Commissioning of Electric Water Heater	7	18-Nov-26	26-Nov-26	30-Dec-26	06-Jan-27	2,987.25	0.00	0.00	0%	0%		Testing

Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary

Date	Revision	Checked	Approved
06-Oct-26	Weekly Report		

Activity ID	Activity Name	Original Duration	BL Project Start	BL Project Finish	Start	Finish	Budgeted Total Cost	Planned Value Cost	Earned Value Cost	Schedule % Complete	Performance % Complete	2026	2027
P001-C-TC-M-3426	Testing and Commissioning of Sanitary Fixtures	7	23-Nov-26	01-Dec-26	04-Jan-27	11-Jan-27	32,707.31	0.00	0.00	0%	0%		Testing
P001-C-TC-M-3376	Testing and Commissioning of Fire Fighting Pipes	7	02-Dec-26	10-Dec-26	19-Jan-27	26-Jan-27	118,857.06	0.00	0.00	0%	0%		Testin
P001-C-TC-M-3396	Testing & Commissioning of Water Supply Pipes	7	29-Nov-26	07-Dec-26	19-Jan-27	26-Jan-27	38,283.97	0.00	0.00	0%	0%		Testin
P001-C-TC-M3446	Testing and Commissioning of Exhaust Fan	7	26-Nov-26	05-Dec-26	21-Jan-27	28-Jan-27	13,737.46	0.00	0.00	0%	0%		Testin
P001-C-TC-M-3456	Testing and Commissioning of Wall propeller type exhaust fans	7	01-Dec-26	09-Dec-26	26-Jan-27	02-Feb-27	76,887.76	0.00	0.00	0%	0%		Testin
P001-C-TC-M-3436	Testing and Commissioning of HVAC Duct	7	03-Dec-26	12-Dec-26	28-Jan-27	04-Feb-27	245,430.24	0.00	0.00	0%	0%		Testin
P001-C-TC-M-3386	Testing and Commissioning of Fire Hose Cabinet	3	10-Jan-27	17-Jan-27	21-Feb-27	24-Feb-27	24,887.19	0.00	0.00	0%	0%		Testi
ELECTRICAL		29	29-Nov-26	18-Feb-27	24-Jan-27	27-Feb-27	1,326,463.06	0.00	0.00	0%	0%		27-F
P001-C-TC-E-3506	Testing and Commissioning of Wiring Devices	7	29-Nov-26	07-Dec-26	24-Jan-27	31-Jan-27	33,207.17	0.00	0.00	0%	0%		Testin
P001-C-TC-E-3496	Testing and Commissioning of Fire Alarm System	2	07-Dec-26	08-Dec-26	02-Feb-27	03-Feb-27	139,733.70	0.00	0.00	0%	0%		Testin
P001-C-TC-E-3466	Testing and Commissioning of Disconnect Switches	7	30-Dec-26	06-Jan-27	07-Feb-27	14-Feb-27	50,288.02	0.00	0.00	0%	0%		Testin
P001-C-TC-E-3546	Testing and Commissioning of Access Control System	2	17-Dec-26	19-Dec-26	10-Feb-27	11-Feb-27	45,341.12	0.00	0.00	0%	0%		Testin
P001-C-TC-E-3486	Testing and Commissioning of Grounding	2	26-Dec-26	27-Dec-26	14-Feb-27	16-Feb-27	32,570.63	0.00	0.00	0%	0%		Testin
P001-C-TC-E-3456	Testing and Commissioning of Main Distribution Board	3	23-Dec-26	30-Dec-26	16-Feb-27	18-Feb-27	53,313.44	0.00	0.00	0%	0%		Testin
P001-C-TC-E-3446	Testing and Commissioning of LV cables	2	26-Dec-26	27-Dec-26	18-Feb-27	20-Feb-27	149,517.23	0.00	0.00	0%	0%		Testin
P001-C-TC-E-3526	Testing and Commissioning of PP-AC panel	2	26-Dec-26	30-Dec-26	18-Feb-27	20-Feb-27	35,542.28	0.00	0.00	0%	0%		Testin
P001-C-TC-E-3516	Testing and Commissioning of LP panel board	2	31-Dec-26	02-Jan-27	20-Feb-27	21-Feb-27	30,214.76	0.00	0.00	0%	0%		Testin
P001-C-TC-E-3566	Testing and Commissioning of CCTV System	2	29-Dec-26	30-Dec-26	20-Feb-27	21-Feb-27	125,349.49	0.00	0.00	0%	0%		Testin
P001-C-TC-E-3536	Testing and Commissioning of Telephone and data system	2	28-Dec-26	02-Jan-27	21-Feb-27	23-Feb-27	44,313.72	0.00	0.00	0%	0%		Testin
P001-C-TC-E-3556	Testing and Commissioning of Solar power plant	2	17-Feb-27	18-Feb-27	24-Feb-27	27-Feb-27	415,814.30	0.00	0.00	0%	0%		Testi
P001-C-TC-E-3476	Testing and Commissioning of Lighting Fixtures	1	18-Jan-27	18-Jan-27	25-Feb-27	25-Feb-27	171,257.21	0.00	0.00	0%	0%		Testin
TESTING AND COMMISSIONING SITE INFRASTRUCTURE		83	06-Oct-26	06-Feb-27	22-Nov-26	27-Feb-27	530,478.84	0.00	0.00	0%	0%		27-F
PUMP ROOM SHED		23	12-Dec-26	06-Feb-27	09-Dec-26	04-Jan-27	306,247.54	0.00	0.00	0%	0%		04-Jan
S001-C-TC-M-3596	Testing & Commissioning of GRP tank	3	12-Dec-26	14-Dec-26	09-Dec-26	12-Dec-26	104,926.55	0.00	0.00	0%	0%		Testing
S001-C-TC-M-3576	Testing & Commissioning of Fire Fighting pump	5	05-Jan-27	10-Jan-27	14-Dec-26	19-Dec-26	51,684.47	0.00	0.00	0%	0%		Testing
S001-C-TC-M-3586	Testing & Commissioning of Booster pump	7	31-Dec-26	07-Jan-27	14-Dec-26	21-Dec-26	6,462.23	0.00	0.00	0%	0%		Testing
S001-C-TC-E-3616	Testing and Commissioning of Panel Board	2	07-Jan-27	09-Jan-27	16-Dec-26	17-Dec-26	36,675.69	0.00	0.00	0%	0%		Testing
S001-C-TC-E-3636	Testing and Commissioning of Grounding	5	09-Jan-27	13-Jan-27	20-Dec-26	24-Dec-26	208.86	0.00	0.00	0%	0%		Testing
S001-C-TC-E-3646	Testing and Commissioning of Wiring devices	2	13-Jan-27	14-Jan-27	22-Dec-26	23-Dec-26	193.73	0.00	0.00	0%	0%		Testing
S001-C-TC-E-3621	Testing and Commissioning of LV cables	3	19-Jan-27	24-Jan-27	28-Dec-26	30-Dec-26	76,378.12	0.00	0.00	0%	0%		Testing
S001-C-TC-E-3626	Testing and Commissioning of Lighting Fixtures	2	18-Jan-27	19-Jan-27	29-Dec-26	30-Dec-26	1,429.61	0.00	0.00	0%	0%		Testing
S001-C-TC-E-3656	Testing and Commissioning of Programmable Logic Controller	2	26-Jan-27	06-Feb-27	03-Jan-27	04-Jan-27	28,288.27	0.00	0.00	0%	0%		Testing
EXTERNAL		26	18-Nov-26	09-Dec-26	13-Jan-27	13-Feb-27	52,779.67	0.00	0.00	0%	0%		13-Fe
S001-C-TC-EX-E-3646	Testing and Commissioning of Street Lighting pole	15	22-Nov-26	08-Dec-26	13-Jan-27	31-Jan-27	35,084.37	0.00	0.00	0%	0%		Testin
S001-C-TC-EX-E-3626	Testing and Commissioning of LV cables	7	18-Nov-26	25-Nov-26	21-Jan-27	30-Jan-27	14,763.42	0.00	0.00	0%	0%		Testin
S001-C-TC-EX-E-3656	Testing and Commissioning of Grounding	7	02-Dec-26	09-Dec-26	04-Feb-27	13-Feb-27	2,931.87	0.00	0.00	0%	0%		Testin
ENVIRONMENTAL		83	06-Oct-26	19-Jan-27	22-Nov-26	27-Feb-27	171,451.64	0.00	0.00	0%	0%		27-F
S001-C-TC-ENV-F-1051	Testing & Commissioning of External Fire Fighting System 200 Dia	15	06-Oct-26	22-Oct-26	22-Nov-26	09-Dec-26	72,486.43	0.00	0.00	0%	0%		Testing
S001-C-TC-ENV-WS-11	Testing & Commissioning of Water Supply System	15	22-Nov-26	08-Dec-26	24-Dec-26	10-Jan-27	5,327.52	0.00	0.00	0%	0%		Testing
S001-C-TC-ENV-SW-70	Testing & Commissioning of Irrigaiton System	15	15-Dec-26	31-Dec-26	25-Jan-27	10-Feb-27	11,300.41	0.00	0.00	0%	0%		Testin
S001-C-TC-ENV-3666	Testing and Commissioning of Main program system & controller	10	23-Dec-26	09-Jan-27	02-Feb-27	13-Feb-27	14,943.05	0.00	0.00	0%	0%		Testin
S001-C-TC-ENV-SW-60	Testing & Commissioning of Sewer & Drainage System	3	03-Jan-27	19-Jan-27	24-Feb-27	27-Feb-27	67,394.23	0.00	0.00	0%	0%		Testi
SNAGG WORKS		79	10-Jun-26	16-Jul-26	17-Jun-26 A	06-Jul-26 A	7,125,585.81	7,125,585.81	7,125,585.81	100%	100%		06-Jul-26 A,
S001-C-TC-C-80	Civil & Architectural Snagg works-1	5	05-Jul-26	11-Jul-26	17-Jun-26 A	20-Jun-26 A	1,520,575.29	1,520,575.29	1,520,575.29	100%	100%		Civil & Archite
S001-C-TC-A-90	Civil & Architectural Snagg works-2	5	11-Jul-26	16-Jul-26	21-Jun-26 A	22-Jun-26 A	1,000,000.00	1,000,000.00	1,000,000.00	100%	100%		Civil & Archite
S001-C-TC-E-3676	External Snagg works	5	02-Jul-26	07-Jul-26	22-Jun-26 A	05-Jul-26 A	3,231,301.32	3,231,301.32	3,231,301.32	100%	100%		External Sna
S001-C-TC-M-100	Mechanical Snagg works	5	10-Jun-26	15-Jun-26	05-Jul-26 A	06-Jul-26 A	1,206,604.05	1,206,604.05	1,206,604.05	100%	100%		Mechanical
S001-C-TC-E-3606	Electrical Snagg works	5	08-Jul-26	13-Jul-26	05-Jul-26 A	06-Jul-26 A	167,105.15	167,105.15	167,105.15	100%	100%		Electrical Sn
PREOJECT CLOSEOUT		21	02-Feb-27	06-Mar-27	09-Feb-27	06-Mar-27	0.00	0.00	0.00	0%	0%		06-M

Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary

Date	Revision	Checked	Approved
06-Oct-26	Weekly Report		

Activity ID	Activity Name	Original Duration	BL Project Start	BL Project Finish	Start	Finish	Budgeted Total Cost	Planned Value Cost	Earned Value Cost	Schedule % Complete	Performance % Complete	2026	2027
ENGINEERING		8	02-Feb-27	10-Feb-27	09-Feb-27	18-Feb-27	0.00	0.00	0.00	0%	0%		18-Fe
AS BUILT DRAWINGS		6	02-Feb-27	08-Feb-27	09-Feb-27	16-Feb-27	0.00	0.00	0.00	0%	0%		16-Fe
CIVIL DRAWINGS		2	02-Feb-27	03-Feb-27	09-Feb-27	11-Feb-27	0.00	0.00	0.00	0%	0%		11-Fe
PREPARATION AND SUBMITTALS		2	02-Feb-27	03-Feb-27	09-Feb-27	11-Feb-27	0.00	0.00	0.00	0%	0%		11-Fe
DAM3-AB-1010	Civil drawings	2	02-Feb-27	03-Feb-27	09-Feb-27	11-Feb-27	0.00	0.00	0.00	0%	0%		Civil d
REVIEW AND APPROVALS		2	02-Feb-27	03-Feb-27	09-Feb-27	11-Feb-27	0.00	0.00	0.00	0%	0%		11-Fe
DAM3-AB-1053	Civil drawings	2	02-Feb-27	03-Feb-27	09-Feb-27	11-Feb-27	0.00	0.00	0.00	0%	0%		Civil d
ARCHITECTURAL DRAWINGS		4	04-Feb-27	08-Feb-27	11-Feb-27	16-Feb-27	0.00	0.00	0.00	0%	0%		16-Fe
PREPARATION AND SUBMITTALS		2	04-Feb-27	06-Feb-27	11-Feb-27	14-Feb-27	0.00	0.00	0.00	0%	0%		14-Fe
DAM3-AB-1011	Architectural drawings	2	04-Feb-27	06-Feb-27	11-Feb-27	14-Feb-27	0.00	0.00	0.00	0%	0%		Archi
REVIEW AND APPROVALS		2	07-Feb-27	08-Feb-27	14-Feb-27	16-Feb-27	0.00	0.00	0.00	0%	0%		16-Fe
DAM3-AB-1023	Architectural drawings	2	07-Feb-27	08-Feb-27	14-Feb-27	16-Feb-27	0.00	0.00	0.00	0%	0%		Archi
MECHANICAL DRAWINGS		4	04-Feb-27	08-Feb-27	11-Feb-27	16-Feb-27	0.00	0.00	0.00	0%	0%		16-Fe
PREPARATION AND SUBMITTALS		2	04-Feb-27	06-Feb-27	11-Feb-27	14-Feb-27	0.00	0.00	0.00	0%	0%		14-Fe
DAM3-AB-1013	Mechanical drawings	2	04-Feb-27	06-Feb-27	11-Feb-27	14-Feb-27	0.00	0.00	0.00	0%	0%		Mech
REVIEW AND APPROVALS		2	07-Feb-27	08-Feb-27	14-Feb-27	16-Feb-27	0.00	0.00	0.00	0%	0%		16-Fe
DAM3-AB-1033	Mechanical drawings	2	07-Feb-27	08-Feb-27	14-Feb-27	16-Feb-27	0.00	0.00	0.00	0%	0%		Mech
ELECTRICAL DRAWINGS		4	04-Feb-27	08-Feb-27	11-Feb-27	16-Feb-27	0.00	0.00	0.00	0%	0%		16-Fe
PREPARATION AND SUBMITTALS		2	04-Feb-27	06-Feb-27	11-Feb-27	14-Feb-27	0.00	0.00	0.00	0%	0%		14-Fe
DAM3-AB-1012	Electrical drawings	2	04-Feb-27	06-Feb-27	11-Feb-27	14-Feb-27	0.00	0.00	0.00	0%	0%		Electr
REVIEW AND APPROVALS		2	07-Feb-27	08-Feb-27	14-Feb-27	16-Feb-27	0.00	0.00	0.00	0%	0%		16-Fe
DAM3-AB-1043	Electrical drawings	2	07-Feb-27	08-Feb-27	14-Feb-27	16-Feb-27	0.00	0.00	0.00	0%	0%		Electr
EXTERNAL WORKS DRAWINGS		4	04-Feb-27	08-Feb-27	11-Feb-27	16-Feb-27	0.00	0.00	0.00	0%	0%		16-Fe
PREPARATION AND SUBMITTALS		2	04-Feb-27	06-Feb-27	11-Feb-27	14-Feb-27	0.00	0.00	0.00	0%	0%		14-Fe
DAM3-AB-1054	External works drawings	2	04-Feb-27	06-Feb-27	11-Feb-27	14-Feb-27	0.00	0.00	0.00	0%	0%		Exter
REVIEW AND APPROVALS		2	07-Feb-27	08-Feb-27	14-Feb-27	16-Feb-27	0.00	0.00	0.00	0%	0%		16-Fe
DAM3-AB-1055	External works drawings	2	07-Feb-27	08-Feb-27	14-Feb-27	16-Feb-27	0.00	0.00	0.00	0%	0%		Exter
WARRANTIES AND GUARANTEES		4	07-Feb-27	10-Feb-27	14-Feb-27	18-Feb-27	0.00	0.00	0.00	0%	0%		18-Fe
SYSTEM		4	07-Feb-27	10-Feb-27	14-Feb-27	18-Feb-27	0.00	0.00	0.00	0%	0%		18-Fe
PREPARATION AND SUBMITTALS		2	07-Feb-27	08-Feb-27	14-Feb-27	16-Feb-27	0.00	0.00	0.00	0%	0%		16-Fe
DAM3-WG-1010	Warraties and Guarantees For Mechanical Equipments	2	07-Feb-27	08-Feb-27	14-Feb-27	16-Feb-27	0.00	0.00	0.00	0%	0%		Warra
DAM3-WG-1011	Warraties and Guarantees For Electrical Systems	2	07-Feb-27	08-Feb-27	14-Feb-27	16-Feb-27	0.00	0.00	0.00	0%	0%		Warra
REVIEW AND APPROVAL		2	09-Feb-27	10-Feb-27	16-Feb-27	18-Feb-27	0.00	0.00	0.00	0%	0%		18-Fe
DAM3-WG-1012	Warraties and Guarantees For Mechanical Equipments	2	09-Feb-27	10-Feb-27	16-Feb-27	18-Feb-27	0.00	0.00	0.00	0%	0%		Warra
DAM3-WG-1013	Warraties and Guarantees For Electrical Systems	2	09-Feb-27	10-Feb-27	16-Feb-27	18-Feb-27	0.00	0.00	0.00	0%	0%		Warra
TRAINING AND MANUALS		10	11-Feb-27	23-Feb-27	18-Feb-27	03-Mar-27	0.00	0.00	0.00	0%	0%		03-M
TRAINING		6	11-Feb-27	17-Feb-27	18-Feb-27	27-Feb-27	0.00	0.00	0.00	0%	0%		27-Fe
SYSTEM		6	11-Feb-27	17-Feb-27	18-Feb-27	27-Feb-27	0.00	0.00	0.00	0%	0%		27-Fe
PREPARATION AND SUBMITTALS		2	11-Feb-27	13-Feb-27	18-Feb-27	21-Feb-27	0.00	0.00	0.00	0%	0%		21-Fe
DAM3-WG-1014	The Proposed Coursework For Mechanical Equipment	2	11-Feb-27	13-Feb-27	18-Feb-27	21-Feb-27	0.00	0.00	0.00	0%	0%		The P
DAM3-WG-1015	The Proposed Coursework For Electircal systems	2	11-Feb-27	13-Feb-27	18-Feb-27	21-Feb-27	0.00	0.00	0.00	0%	0%		The P
REVIEW AND APPROVAL		2	14-Feb-27	15-Feb-27	21-Feb-27	24-Feb-27	0.00	0.00	0.00	0%	0%		24-Fe
DAM3-WG-1016	The Proposed Coursework For Mechanical Equipment	2	14-Feb-27	15-Feb-27	21-Feb-27	24-Feb-27	0.00	0.00	0.00	0%	0%		The P
DAM3-WG-1017	The Proposed Coursework For Electircal systems	2	14-Feb-27	15-Feb-27	21-Feb-27	24-Feb-27	0.00	0.00	0.00	0%	0%		The P
DELIVERY		2	16-Feb-27	17-Feb-27	24-Feb-27	27-Feb-27	0.00	0.00	0.00	0%	0%		27-Fe
DAM3-WG-1018	The Proposed Coursework For Mechanical Equipment	2	16-Feb-27	17-Feb-27	24-Feb-27	27-Feb-27	0.00	0.00	0.00	0%	0%		The P
DAM3-WG-1019	The Proposed Coursework For Electircal systems	2	16-Feb-27	17-Feb-27	24-Feb-27	27-Feb-27	0.00	0.00	0.00	0%	0%		The P
MANUALS		4	18-Feb-27	23-Feb-27	27-Feb-27	03-Mar-27	0.00	0.00	0.00	0%	0%		03-M
SYSTEM		4	18-Feb-27	23-Feb-27	27-Feb-27	03-Mar-27	0.00	0.00	0.00	0%	0%		03-M

Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary

Date	Revision	Checked	Approved
06-Oct-26	Weekly Report		

Activity ID	Activity Name	Original Duration	BL Project Start	BL Project Finish	Start	Finish	Budgeted Total Cost	Planned Value Cost	Earned Value Cost	Schedule % Complete	Performance % Complete	2026	2027
PREPARATION AND SUBMITTALS		2	18-Feb-27	20-Feb-27	27-Feb-27	01-Mar-27	0.00	0.00	0.00	0%	0%		▼ 01-M
DAM3-WG-1020	Manual and Catalogue For Mechanical Equipment	2	18-Feb-27	20-Feb-27	27-Feb-27	01-Mar-27	0.00	0.00	0.00	0%	0%		Mani
DAM3-WG-1021	Manual and Catalogue For For Electircal systems	2	18-Feb-27	20-Feb-27	27-Feb-27	01-Mar-27	0.00	0.00	0.00	0%	0%		Mani
REVIEW AND APPROVAL		2	21-Feb-27	23-Feb-27	01-Mar-27	03-Mar-27	0.00	0.00	0.00	0%	0%		▼ 03-M
DAM3-WG-1022	Manual and Catalogue For Mechanical Equipment	2	21-Feb-27	23-Feb-27	01-Mar-27	03-Mar-27	0.00	0.00	0.00	0%	0%		Mani
DAM3-WG-1023	Manual and Catalogue For For Electircal systems	2	21-Feb-27	23-Feb-27	01-Mar-27	03-Mar-27	0.00	0.00	0.00	0%	0%		Mani
DEMOBILIZATION		13	09-Feb-27	24-Feb-27	16-Feb-27	04-Mar-27	0.00	0.00	0.00	0%	0%		▼ 04-M
DAM3-D.MOB-1013	Demobilization of manpower	2	09-Feb-27	10-Feb-27	16-Feb-27	18-Feb-27	0.00	0.00	0.00	0%	0%		Demo
DAM3-D.MOB-1020	Demobilization of equipment	2	11-Feb-27	13-Feb-27	18-Feb-27	21-Feb-27	0.00	0.00	0.00	0%	0%		Demo
DAM3-D.MOB-1010	Dismantling and removal offices	1	24-Feb-27	24-Feb-27	03-Mar-27	04-Mar-27	0.00	0.00	0.00	0%	0%		Dism
FINAL HANDOVER		5	23-Feb-27	06-Mar-27	01-Mar-27	06-Mar-27	0.00	0.00	0.00	0%	0%		▼ 06-M
DAM3-FH-1000	Snag List Rectification	3	23-Feb-27	03-Mar-27	01-Mar-27	03-Mar-27	0.00	0.00	0.00	0%	0%		Snag
DAM3-FH-1010	Handover Letter	1	04-Mar-27	04-Mar-27	04-Mar-27	04-Mar-27	0.00	0.00	0.00	0%	0%		Hand
DAM3-FH-1020	Intial Handingover	1	06-Mar-27	06-Mar-27	06-Mar-27	06-Mar-27	0.00	0.00	0.00	0%	0%		Intia

Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary

Date	Revision	Checked	Approved
06-Oct-26	Weekly Report		
