Development of Infrastructure Networks, 3rd Industrial City in Dammam, Phase 2 Part 2, Zone J

تطوير شبكات البنية التحتية للمدينة الصناعية الثالثة بالدمام المرحلة الثانية الجزء الثاني - المنطقة J

CLIENT	CONTRACTOR	CONSULTANT	MODON PM	SITE HANDOVER	CONTRACT COMPLETION
MODON	ANSAB General Contracting	EGIS	Eng. Mohammed Al-Aissa	12-Jan-2025	11-Jan-2027

Scope: collector and local roads, potable water, sewerage, storm drainage, irrigation, medium-voltage, street lighting and telecom networks, a sewage pump station and storm drainage ponds for Block J. Contract value 117.4M SAR excluding VAT, 24 months.

Status at a glance

Progress is measured as physical % complete, weighted by budgeted effort (man-days, the same basis as report 94). At the 03-Nov-2026 data date the project is 78.7% complete against 87.6% planned, behind by 8.9% (SPI 0.90). Since report 94 it gained 0.24% against 1.04% planned, so the gap widened again.

PHYSICAL % COMPLETE

78.7% / 87.6% plan

▼ SPI 0.90 −8.9%

PROGRESS THIS WEEK

+0.24% / +1.04% plan

▼ 0.8% below the weekly plan

CONTRACT TIME ELAPSED

90.5% · day 660 of 729

▼ P6 finish 20-Nov-2027

INVOICED TO DATE (GROSS)

43.1% · 50.6M SAR

20 invoices, last period ends 30-Sep-2026

The project is now forecast to finish eight to ten months late.

The P6 update of 03-Nov-2026 finishes the project on 20-Nov-2027, 313 days after the contract date of 11-Jan-2027, with −258 days of float. The weekly report forecasts 29-Sep-2027 (261 days late), the date the failed-start list also shows. Report 94's revised forecast of 18-Jan-2027 has been withdrawn. With 90.5% of the contract time used, 21.3% of the physical work remains, and every network completion milestone is between 196 and 258 days negative in P6.

Site photos this week

Four new photos uploaded with report 95, camera-stamped 31-Oct to 04-Nov-2026, 3rd Industrial City, Dammam. They show backfilling around the lift station walls, a barricaded deep excavation and the road formation. Select a photo to view it larger, then use the arrows to move between photos.




Backfilling at the lift station

Roller compacting backfill against the protected wall. Stamped 31-Oct-2026, 08:24.




Deep excavation barricaded

Concrete barriers and a deep-excavation sign around an open chamber. Stamped 03-Nov-2026, 11:24.

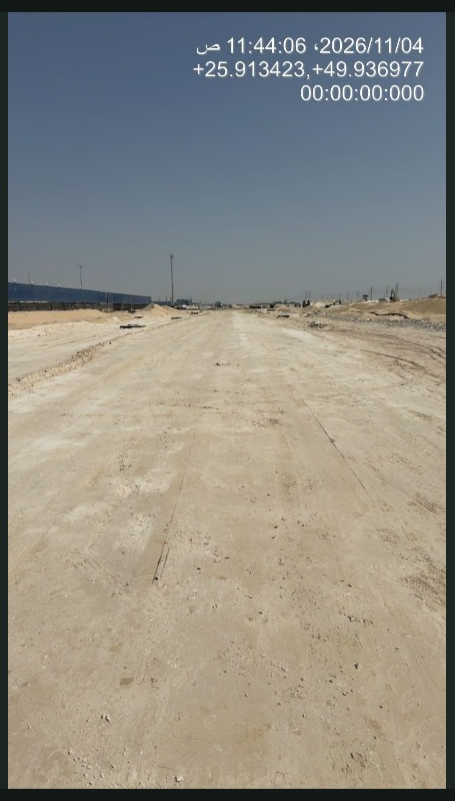

Road formation

Graded formation along the road corridor. GPS-stamped 04-Nov-2026, 11:44.

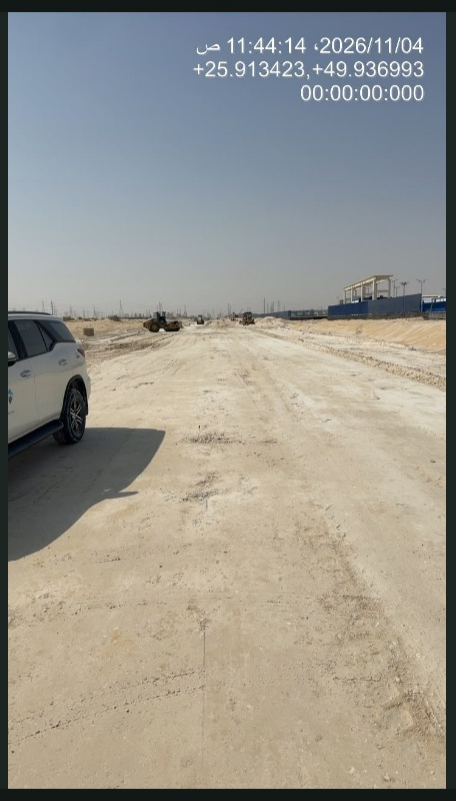


Road corridor

Formation ready for the next layer, equipment working further along. GPS-stamped 04-Nov-2026, 11:44.

Progress S-curve

Cumulative physical progress (effort weighted), monthly. Source: Physical-Chart Data sheet.

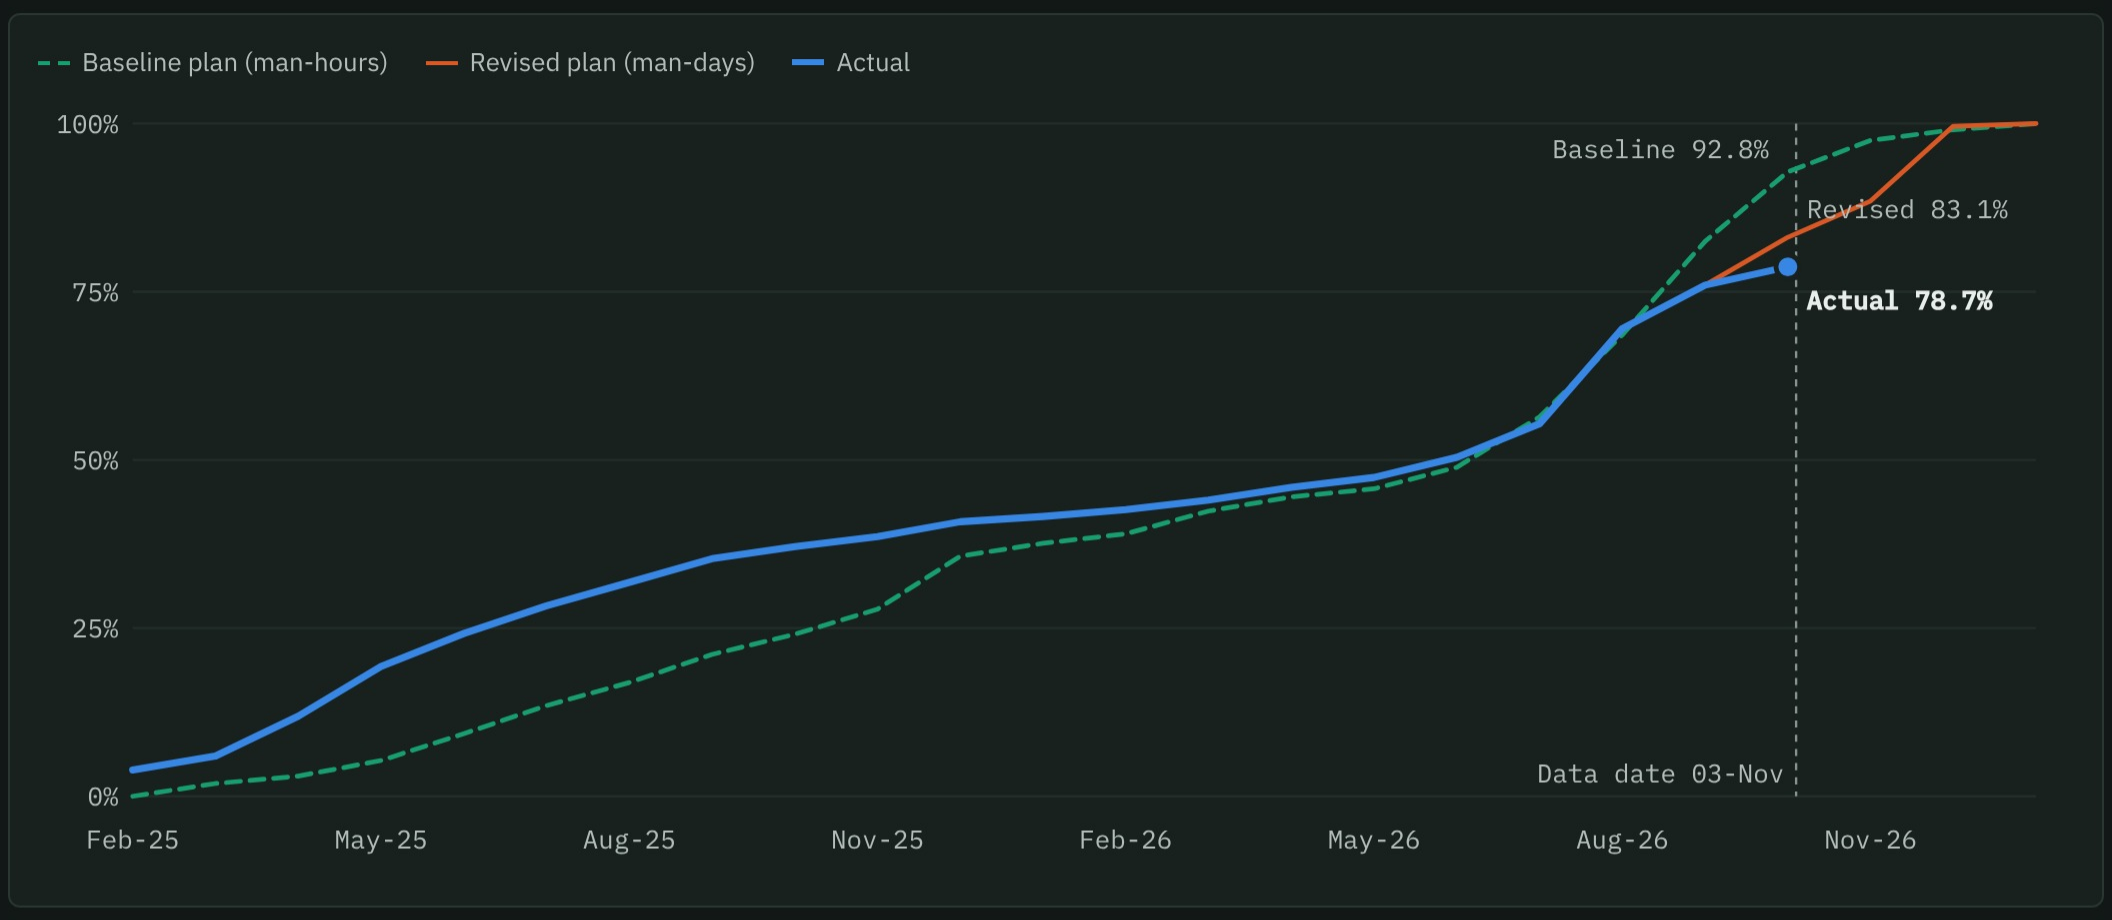

PERIOD ENDING	PLANNED %	ACTUAL %	VARIANCE	GAINED IN PERIOD	SPI
Jul-2026	55.4	55.4	0.0	+5.0	1.00
Aug-2026	69.5	69.5	0.0	+14.1	1.00
Sep-2026	76.0	76.0	0.0	+6.5	1.00
27-Oct-2026	86.6*	78.5	−8.1	+2.5	0.91
03-Nov-2026	**87.6***	**78.7**	**−8.9**	**+0.2**	**0.90**

Month-end values against the revised plan (man-days) from the Physical-Chart Data sheet, then report 94 (previous week, same basis) and report 95. Up to September the sheet's actual equals the revised plan exactly, so SPI shows 1.00. * Planned value at the data date from the Progress sheet; the revised plan for the end of October is 83.1%, lower than both. The original man-hour baseline called for 92.8% by the end of October.

Progress by phase

Physical progress to date by WBS, weighted by budgeted effort (man-days). Source: Progress sheet.


PHASE	WEIGHT	PLANNED	ACTUAL	VARIANCE	SPI	STATUS
Engineering	3.0%	100.0%	100.0%	0.0	1.00	✓ Complete
Procurement	20.0%	100.0%	95.4%	−4.6	0.95	▼ Behind
Earthworks network	6.8%	100.0%	100.0%	0.0	1.00	✓ Complete
Irrigation network	1.9%	100.0%	53.7%	−46.3	0.54	▼ Behind
Potable water network	2.9%	99.7%	68.7%	−31.0	0.69	▼ Behind
Medium-voltage network	1.6%	100.0%	94.4%	−5.6	0.94	▼ Behind
Street lighting network	3.7%	100.0%	9.4%	−90.6	0.09	▼ Behind
Telecom network	1.5%	100.0%	61.7%	−38.3	0.62	▼ Behind
Roads network	23.1%	91.3%	64.8%	−26.5	0.71	▼ Behind

PHASE	WEIGHT	PLANNED	ACTUAL	VARIANCE	SPI	STATUS
Sewage network	12.7%	98.1%	87.4%	−10.7	0.89	▼ Behind
Storm drainage network	12.8%	99.2%	84.1%	−15.1	0.85	▼ Behind
Testing & commissioning	10.0%	0.0%	72.4%	+72.4	–	? No plan to date
Total	100%	**87.6%**	**78.7%**	**−8.9**	**0.90**	▼ Behind

Effort is measured in man-days (65,420 in total) on the same basis as report 94, but the line items were re-weighted: mobilisation was dropped and engineering, procurement, the networks and testing changed budgets. This week the report states 778 man-days earned (561 of them in testing and commissioning) against 912 planned; the cumulative earned total rose by only 158, because procurement fell from 12,670 to 12,485 and roads from 10,205 to 9,798. The P6 update (data date 03-Nov-2026) has 1,921 activities: 1,231 completed, 63 in progress and 627 not started. Its scheduled finish is 20-Nov-2027, 313 days after the contract date.

Scope of work: quantities

Total, executed and remaining quantity of each network, from the execution summary in the Arabic progress summary sheet. Report 95 changed the totals for storm, sewerage and potable water, measures roads in tonnes and adds telecom, so "this week" is shown only where the total is unchanged since report 94.

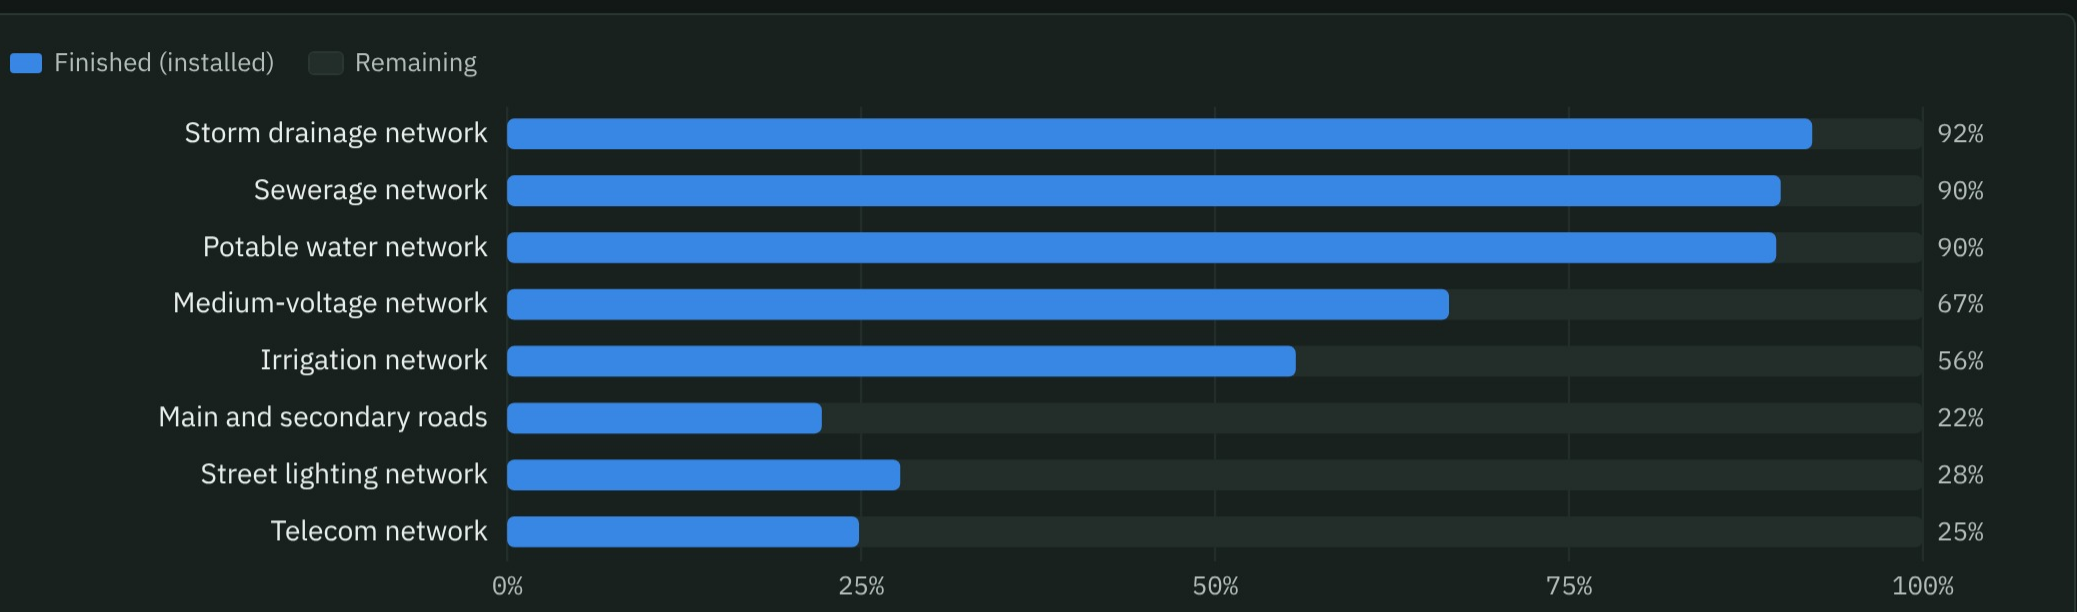

SCOPE ITEM	ZONE	UNIT	TOTAL	FINISHED	THIS WEEK	REMAINING	% FINISHED	BACKFILLED
Storm drainage network	Block J	LM	24,720	22,788	–	1,932	92.2%	–
Sewerage network	Block J	LM	12,806	11,520	–	1,286	90.0%	–
Potable water network	Block J	LM	14,405	12,913	–	1,492	89.6%	–
Medium-voltage network	Block J	LM	17,328	11,528	0	5,800	66.5%	–
Irrigation network	Block J	LM	14,494	8,074	0	6,420	55.7%	–
Main and secondary roads	Block J	t	55,631	12,365	–	43,266	22.2%	–
Street lighting network	Block J	LM	12,786	3,550	0	9,236	27.8%	–
Telecom network	Block J	LM	9,354	2,325	–	7,029	24.9%	–

Work executed this week

NETWORK	ACTIVITY	UNIT	THIS WEEK	SOURCE
Potable water	200 mm water line laid	LM	100	Weekly activities sheet
Medium voltage	MV cable laid	LM	500	Weekly activities sheet
Roads	Capping completed, road 10	LM	500	Weekly activities sheet

NETWORK	ACTIVITY	UNIT	THIS WEEK	SOURCE
Storm drainage	Branch pipes completed, road 23	LM	200	Weekly activities sheet
Road 23	HDPE 315 mm pipes completed	LM	300	Weekly activities sheet
Storm drainage	Manholes and catch basins installed	–	–	Weekly activities sheet
Sewage pump station	Backfilling around the walls	–	–	Weekly activities sheet

Quantities as stated in the report's weekly activities sheet. Planned next: complete the 630 mm water line, the 500 mm irrigation line and the 800 mm line, about 1,000 m of MV cable on street 9, more manholes and catch basins, and asphalt on street 10 and road 14.

Furthest behind

Street lighting is 27.8% executed (3,550 of 12,786 LM) and telecom 24.9% (2,325 of 9,354 LM). Roads are at 22.2% by tonnage (12,365 of 55,631 t), with asphalt still ahead on street 10 and road 14. Irrigation remains at 55.7%. Traffic markings, signs and fire hydrants (0 of 55) have not started.

Close to finished

On the new totals storm drainage is 92.2%, sewerage 90.0% and potable water 89.6% executed. The Major Quantities sheet now shows 8,136 of 8,218 m of 200 mm water pipe laid. The storm box conduit (2,051 m) is complete, and the lift station walls are being backfilled.

Milestones

Baseline and forecast dates from the weekly report's milestone table, against the P6 update of 03-Nov-2026. Days in brackets are the delay the weekly report gives against the baseline.


MILESTONE	BASELINE	WEEKLY REPORT FORECAST	P6 UPDATE FORECAST	P6 FLOAT (DAYS)	STATUS
Site handover	12-Jan-2025	12-Jan-2025	12-Jan-2025 (actual)	–	✓ Done
Complete mobilisation	12-Mar-2025	12-Mar-2025	09-Mar-2025 (actual)	–	✓ Done
Shop drawings and materials approved	10-Feb-2025	11-Feb-2025	24-May-2025 (actual)	–	✓ Done
Earthworks network	24-May-2026	31-May-2025	–	–	✓ Done
Telecom network	28-Sep-2026	28-Mar-2027 (+181 d)	05-Jun-2027	−227	▼ Late
Irrigation network	23-Aug-2026	04-May-2027 (+254 d)	05-Aug-2027	−232	▼ Late
Potable water network	05-Oct-2026	24-Jul-2027 (+292 d)	26-Sep-2027	−257	▼ Late
Sewage network	06-Oct-2026	31-May-2027 (+237 d)	26-Aug-2027	−241	▼ Late
Medium-voltage network	17-Oct-2026	10-Apr-2027 (+175 d)	24-Jun-2027	−196	▼ Late
Road works	21-Oct-2026	14-Sep-2027 (+328 d)	25-Oct-2027	−258	▼ Late
Street lighting network	20-Dec-2026	19-Jun-2027 (+181 d)	11-Aug-2027	−248	▼ Late
Storm drainage network	–	–	15-Sep-2027	−232	▼ Late
Storm drainage ponds	–	–	22-May-2027	−122	▼ Late
Sewage pump station	–	–	12-Jun-2027	−140	▼ Late
Tie-in to existing networks	–	–	25-Oct-2027	−245	▼ Late
Project completion	11-Jan-2027	29-Sep-2027 (+261 d)	20-Nov-2027	−258	▼ Late

The P6 update now finishes about two months later than the weekly report.

The weekly report forecasts completion on 29-Sep-2027 and the networks between 28-Mar and 14-Sep-2027. The P6 update of 03-Nov-2026 is 41 to 93 days later for every network and finishes on 20-Nov-2027; its milestones slipped by 42 to 91 days against the 27-Oct-2026 P6 update. The Employer's NOC for the medium-voltage network is still the only control milestone not achieved, and P6 now schedules it for 27-Jan-2027 with −257 days of float.

Procurement of key materials

Share of the required quantity delivered to site. Source: Procurement sheet, weekly report 95. All listed materials are approved.

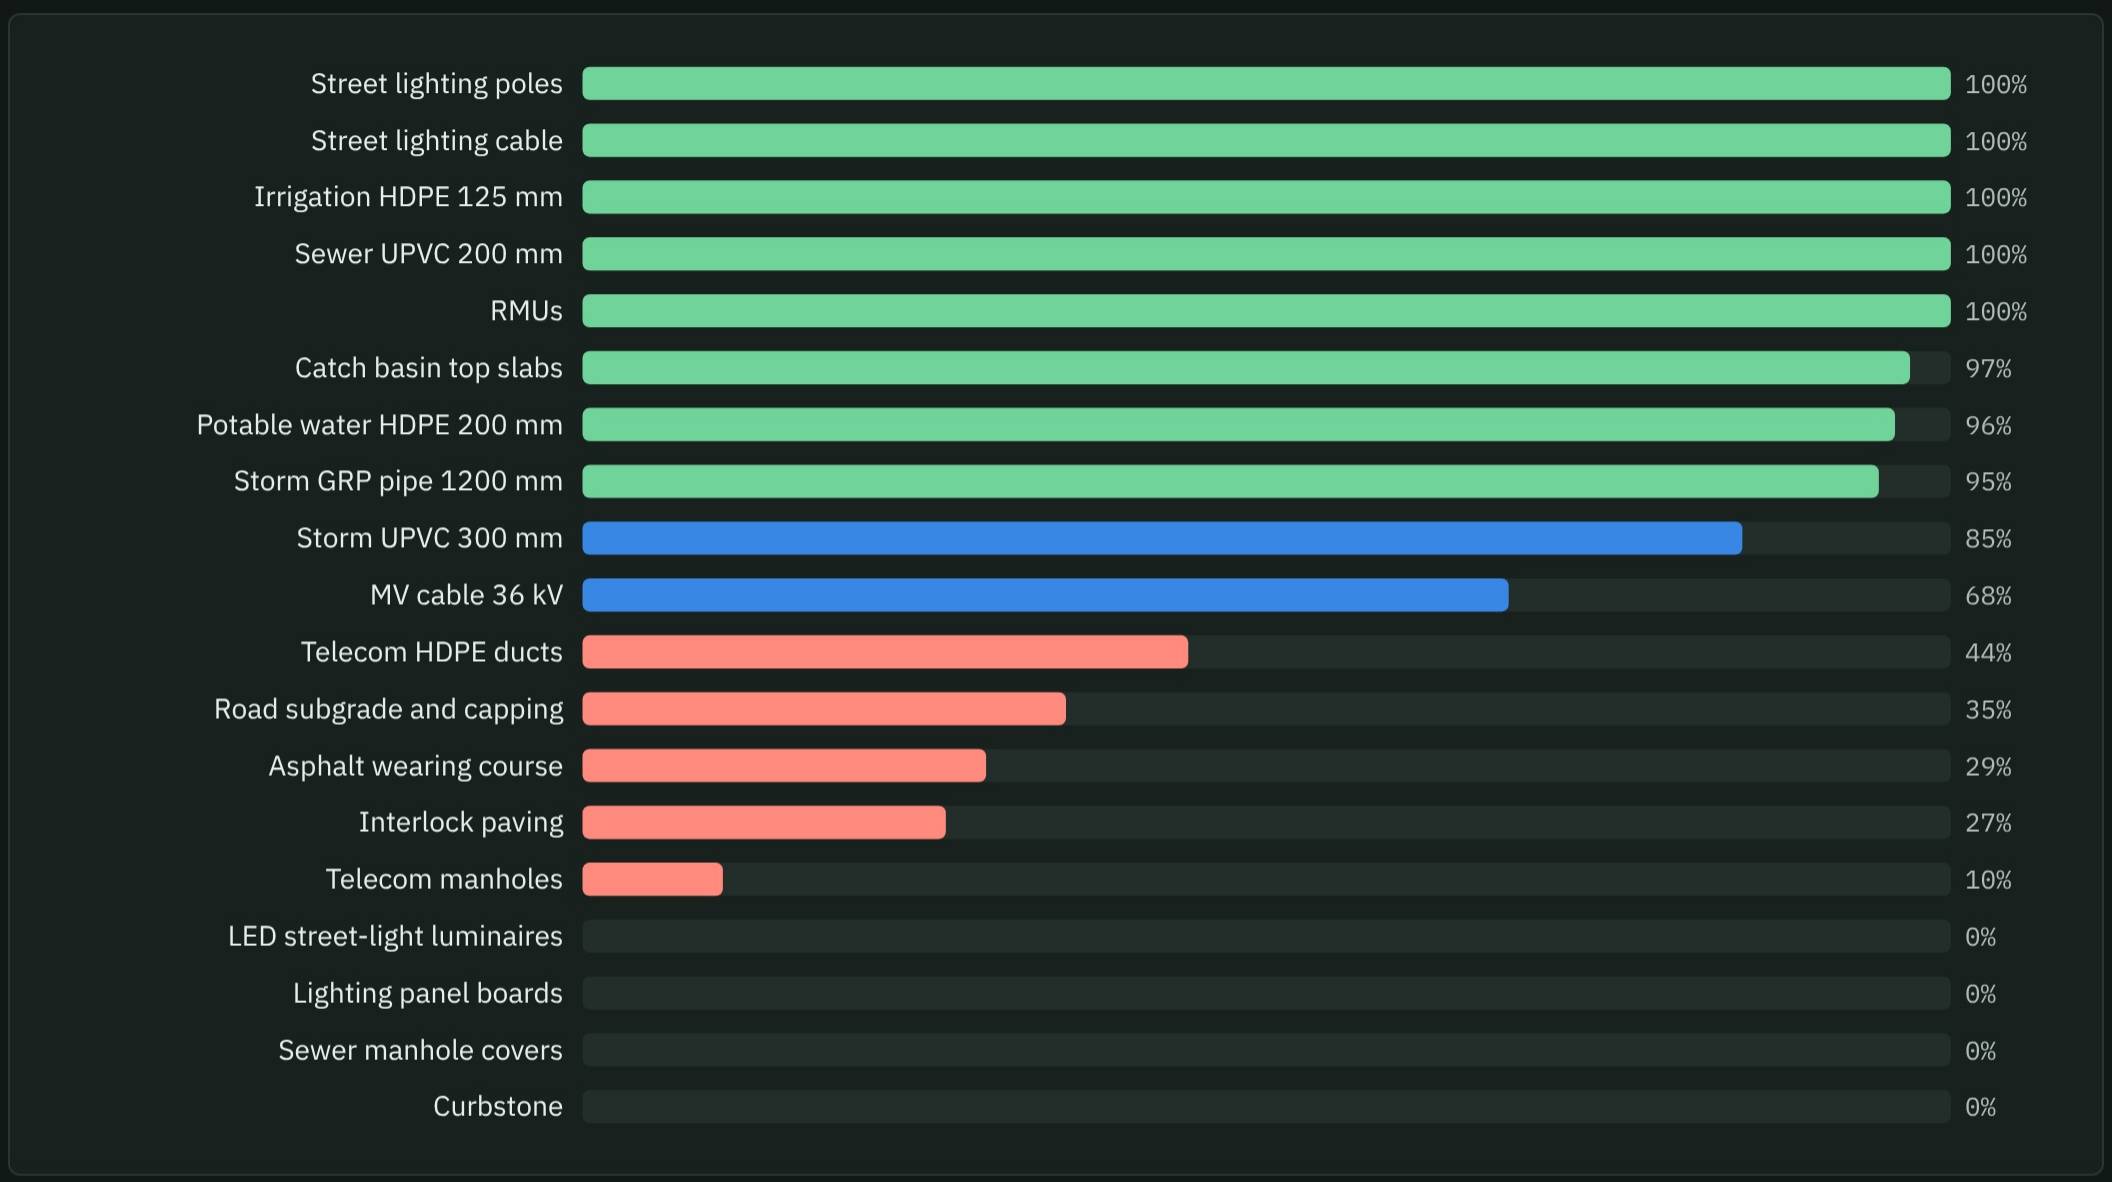

Still nothing delivered for several items


LED street-light luminaires (0 of 363), lighting panel boards (0 of 6), curbstone (0 of 42,552 pieces) and sewer manhole covers (0 of 129). Telecom manholes are at 8 of 78 and telecom ducts at 44%. The register rates delay in long-lead materials as a high risk.

Delivered this week

All 9 RMUs (from 0), the rest of the 125 mm irrigation pipe (now 100%, from 22%), 200 mm sewer pipe (100%), catch-basin top slabs (488 of 503, from 100) and storm manhole bases and rings. Potable water 200 mm pipe is at 96% and storm 300 mm UPVC at 85%. Road-layer materials remain at 17–35%.

Manpower

Head count on site this month by trade, planned vs actual. Source: Manpower sheet. The report has no monthly history.

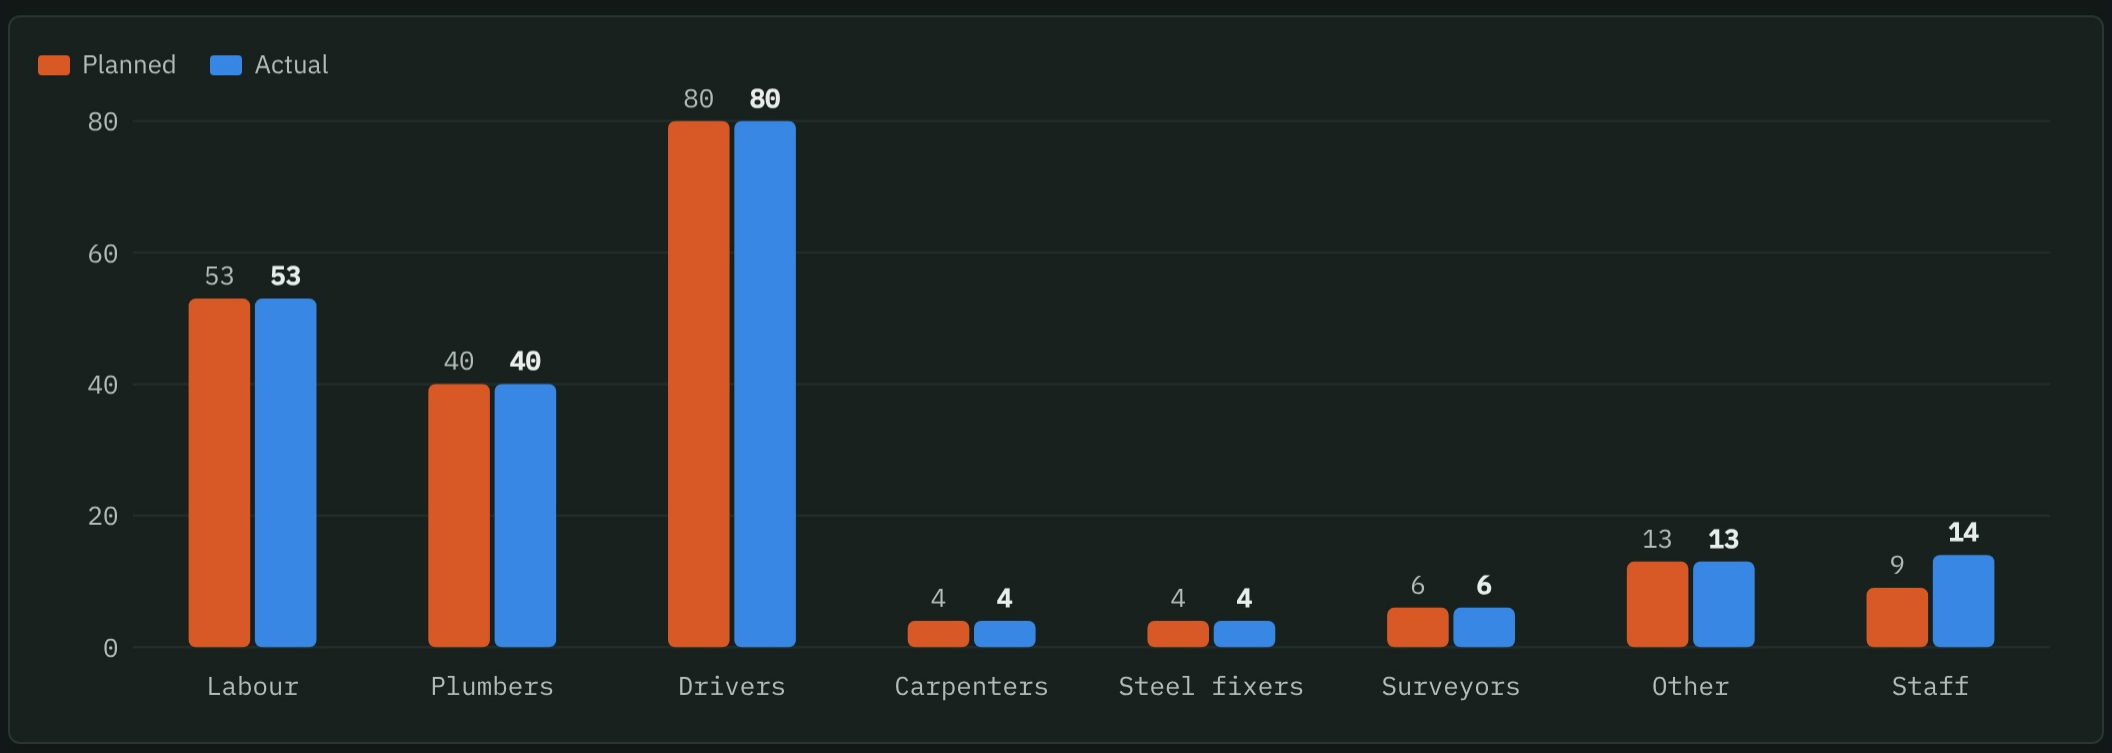

Total head count is 214 against 209 planned: 200 manual workers against 200 and 14 staff against 9. The manpower sheet is unchanged from report 94: every trade's plan equals its actual (for example carpenters and steel fixers 4 each, drivers and operators 80). Equipment on site is 100 units against 78 planned.

Cost and invoicing

Contract value

Roads and paving	31,308,119
Storm water drainage	33,717,595
Sewerage and lift stations	24,177,287
Potable water	10,220,942
Irrigation	6,738,491
Street lighting and telecom	6,440,353
Medium voltage	4,788,987
BOQ total (excl. VAT)	**117,391,774**
Contract value incl. 15% VAT	135,000,540
Change orders	0

All values in SAR. The BOQ total plus 15% VAT matches the contract value. The change order log is empty; the report lists one potential change.

Invoices

Advance payment (10%)	11,739,177
Progress invoices submitted	20
Gross value	50,649,221
Advance payment recovered	5,064,922
Retention / penalties	0 / 0
Approved by MODON PM	50,649,221
Paid (19 invoices)	43,414,468

Invoicing is 43.1% of the contract value against 78.7% physical progress. No new invoice this week. Invoice 20 (01-Sep to 30-Sep-2026, 7,234,753 SAR gross) is approved and awaiting payment.

Health, safety and quality

Safety Score 0.82

Safe man-hours (cumulative)	410,698
Man-hours this week	12,000
Lost-time injuries	0
Fatalities	0
First-aid cases	5
Near misses	1
Property damage	0
Inductions / toolbox talks	106 / 323
Consultant safety inspection, 27-Oct-2026	0.84

Cumulative figures. This week: 10 inductions and 3 toolbox talks.

Quality Score 0.90

FIRs issued (cumulative)	1,881
FIRs closed	1,791
FIRs pending (0–10 days)	90
NCRs issued / closed	21 / 21
Site instructions issued / closed	13 / 12
MIRs issued	0
Shop drawings submitted (all code B)	23
Material submittals (A / B / C / D)	1 / 72 / 2 / 1

NCRs close in 7 days on average. 7 material submittals are still to be approved.

Open issues and risks

ISSUE	OWNER	DETAIL
Schedule delay	Contractor	P6 forecasts completion on 20-Nov-2027, 313 days late (weekly report: 29-Sep-2027, 261 days). Physical progress is 8.9% behind plan and gained only 0.24% this week. The workbook's schedule statistics (406 failed starts, 281 critical-path activities) still repeat report 92's values. No recovery schedule approval is recorded.
Long-lead materials	Contractor	Risk 05, rated high and open: delays in long-lead materials could stop work. Mitigation: chase suppliers and get MODON approval for alternative sources. Target 20-Nov-2026.
Tie-in to existing networks	Contractor / MODON	Risk 01, rated low and open: existing infrastructure may not be ready for the tie-ins, delaying commissioning and handover. P6 tie-in milestone 25-Oct-2027, −245 days of float.
Testing and commissioning	Contractor	Testing was planned to start on 12-Oct-2026 (telecom), 18-Oct-2026 (irrigation) and 26-Oct-2026 (street lighting and medium voltage). None has started; the forecast starts run from 12-Nov-2026 to 04-Jan-2027.
MV network NOC	Contractor	The Employer's NOC for the medium-voltage network is still outstanding (P6: 27-Jan-2027, −257 days).

Closed in the registers: groundwater and dewatering (high), delayed or failed testing, and the two logged issues (irrigation connection point, pump-station force main). The BOQ re-measurement saving is recorded as a realised opportunity.

Data notes

Built from the W06 upload (report 95); the previous week's folder (report 94, updated workbook) was used for this-week changes.

- The workbook's own date fields were not updated: the cover, General Information and Schedule sheets still show data date 27-Oct-2026, report 94 and contract week 93. The file name, the P6 update, the look-ahead and the failed-start list are dated 03-Nov-2026, so this report uses 03-Nov-2026 and week 94 (660 days from handover on 12-Jan-2025).
- Progress basis: report 95 keeps the man-day basis of the updated report 94 (65,420 man-days), and this report uses the same basis. The figures cannot be compared with report 92 (man-hours).
- The cover's physical progress total (89.99% planned, 74.16% earned, SPI 0.82) does not add up: its budget total is 96,167 man-days against 65,420 in the Progress sheet. This report uses the Progress sheet (87.64% planned, 78.71% earned), which the Arabic summary sheet also shows.
- The report states 778 man-days earned this week, but the cumulative earned total rose by only 158 (51,333 to 51,491): procurement fell from 12,670 to 12,485, roads from 10,205 to 9,798, and mobilisation (188) was removed. Testing and commissioning again earns 561 man-days without any planned value or test started.
- Three finish dates disagree: the weekly report and the failed-start list give 29-Sep-2027, the P6 file 20-Nov-2027, and the P6 extract in the Progress sheet shows handover on 07-Feb-2028. The milestone sheet's own schedule extract still lists the 18-Jan-2027 programme from the updated report 94.
- The Arabic summary sheet changed its totals: roads are now in tonnes (55,631 t), storm, sewerage and potable water totals grew (for example storm 18,554 to 24,720 LM) and telecom was added. The Major Quantities sheet changed only for 200 mm water pipe (5,579 to 8,136 m) and lighting poles (126 to 169), while the activities sheet reports 100 m of water line this week.
- The physical forecast in the chart data still reaches 100% in January 2027, against a P6 finish in November 2027. In the chart data the earned effort up to September equals the revised plan month by month.
- Manpower and invoice sheets are unchanged from report 94 (every trade's plan equals its actual; next-month forecast 1,148). HSE hours this week are 12,000 but "this month" shows 6,000, and the HSE inspection sheet still covers 26-Aug to 01-Sep-2026.
- The procurement log still has deliveries above the required quantity (sewer GRP 400 mm SN5000 1,138 of 261 m, potable water 160 mm 214 of 73 m, GRP liner 1,900 mm 43 of 32 m) and unit typos ("m132", "m133").
- The P6 file's project ID is now MOD3-J-2769-BL01-R01-1 (MOD3-J-1 last week). The summary sheet still gives site handover as 12-Feb-2025 (12-Jan-2025 in the weekly report).
- Several cover fields show #REF ! (EAC, top issues), and the invoice log still has stray values of 21,100,000 and 20,900,000.
- Photos: four new photos were uploaded; the other files in the folder repeat earlier weeks' photos and were not reused. Two photos are stamped 04-Nov-2026, a day after the data date.

Compiled 04-Nov-2026 from the W06 upload: weekly report 95 and the P6 update of 03-Nov-2026.
