Completion of the Infrastructure Development of the First Phase, Third Industrial City, Jeddah

إستكمال شبكات البنية التحتية بالمدينة الصناعية الثالثة بجدة

CLIENT	CONTRACTOR	CONSULTANT	MODON PM	SITE HANDOVER	REVISED COMPLETION
MODON	Al-Rawaf Contracting	Egis	Shuaib A. Alshuaibi	29-Jul-2024	26-Sep-2026

Scope: sewage, storm water (with ponds and open channels), irrigation and potable water networks, 13.8 kV cable, street lighting, telecom ducts, and internal and external roads with asphalt and sidewalks.

Status at a glance

Progress is measured as physical % complete, weighted by budgeted man-hours. On 01-Nov-2026 the project is 99.18% complete against 99.93% planned, behind by 0.75% (SPI 0.99). This week gained 0.13% (63 of 48,045 man-hours, in Main Roads and Z05), against 0.09% the week before. The revised completion date of 26-Sep-2026 has passed.

PHYSICAL % COMPLETE

99.2% / 99.9% plan

▼ SPI 0.99 −0.75%

PROGRESS THIS WEEK

+0.13% / 0.00% plan

63 man-hours earned (42 last week); the plan has no progress left for this week

CONTRACT TIME ELAPSED

105% · day 825 of 789

▼ P6 finish 22-Dec-2026

INVOICED TO DATE (GROSS)

84.1% · 268.8M SAR


25 invoices, last period ends 26-Sep-2026

The revised completion date has passed, and both forecasts slipped again: P6 now finishes 87 days late.

The contract completion was extended by two months to 26-Sep-2026 (CCO 2, approved 29-Jun-2026). The weekly report now forecasts completion on 30-Nov-2026, 65 days late (15-Nov-2026 last week). The P6 schedule update of 01-Nov-2026 finishes the project on 22-Dec-2026 with −87 days of total float, a week later than the 15-Dec-2026 (−80 days) of the previous update. In P6 the storm network still finishes zone by zone between 16 and 24-Nov-2026 (Z11, Z04, Z05, Z08), all works including testing and commissioning on 24-Nov-2026, and the approval of all as-built drawings on 08-Nov-2026.

Progress S-curve

Cumulative physical progress (man-hour weighted), monthly. Source: Physical-Chart Data sheet; the 01-Nov-2026 point is from the Progress sheet.

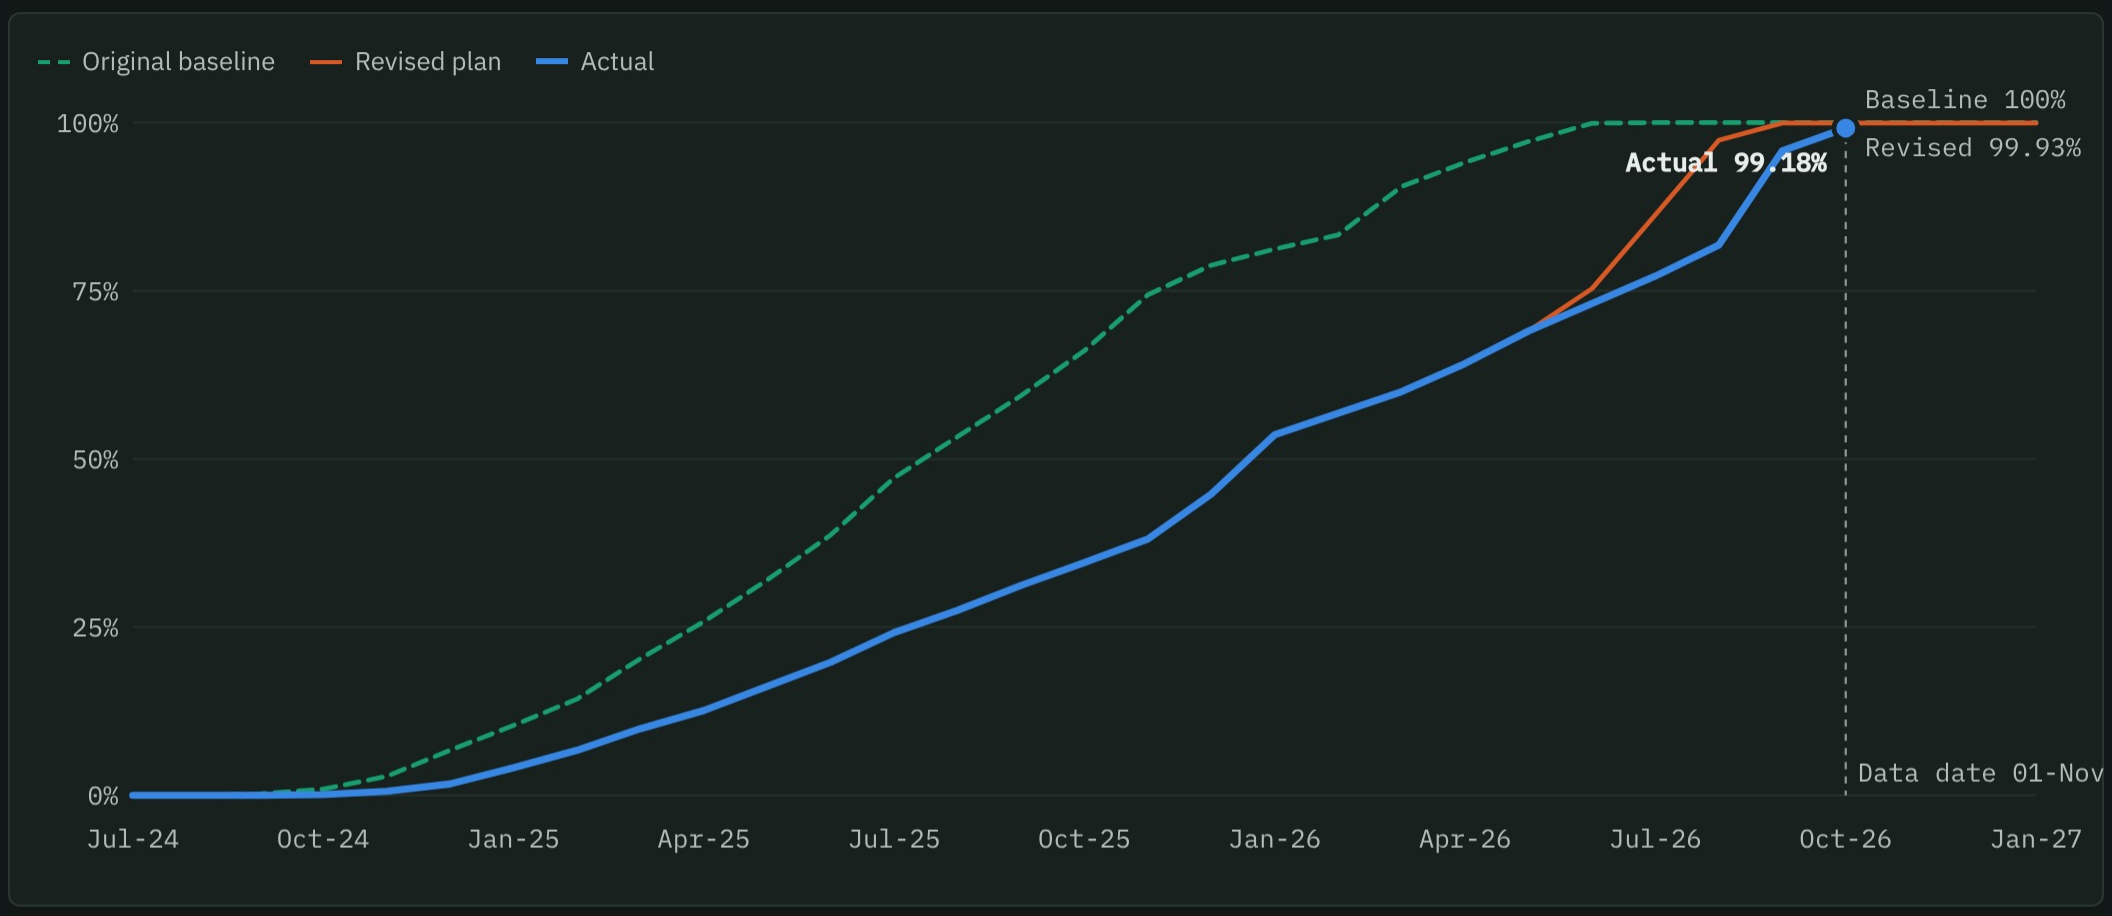

WEEK ENDING	PLANNED %	ACTUAL %	VARIANCE	GAINED THIS WEEK	SPI
18-Oct-2026	99.93	98.96	−0.97	+0.05	0.99
25-Oct-2026	99.93	99.05	−0.88	+0.09	0.99
01-Nov-2026	**99.93**	**99.18**	**−0.75**	**+0.13**	**0.99**

Physical % complete from the weekly reports of 18 Oct, 25 Oct and 01 Nov 2026 (47,547, 47,589 and 47,652 of 48,045 man-hours earned). This week the Physical-Chart Data sheet corrected its actual curve: September now reads 95.8% instead of 100%, and July and August were lowered too. The revised plan ends at 48,012 man-hours (99.93%).

Progress by phase

Physical progress to date by construction work package, weighted by budgeted man-hours (48,045 in total). Engineering, procurement and close-out carry no man-hours, so they have no physical progress figure.


PHASE	WEIGHT	PLANNED	ACTUAL	VARIANCE	SPI	STATUS
MR	36.5%	99.9%	99.8%	−0.1	1.00	▼ Behind
Pond and Swales	7.7%	100.0%	100.0%	0.0	1.00	✓ Complete
Z05	7.7%	100.0%	94.2%	−5.8	0.94	▼ Behind
Z02-2	6.4%	100.0%	100.0%	0.0	1.00	✓ Complete
Z06	6.3%	100.0%	99.6%	−0.4	1.00	▼ Behind
Z01	5.8%	100.0%	100.0%	0.0	1.00	✓ Complete
Z02-1	5.6%	99.4%	100.0%	+0.6	1.01	✓ Complete
Z07	5.6%	100.0%	100.0%	0.0	1.00	✓ Complete
Z07-1	4.3%	100.0%	100.0%	0.0	1.00	✓ Complete
Z10	3.2%	100.0%	99.0%	−1.0	0.99	▼ Behind
High Mast	2.5%	100.0%	100.0%	0.0	1.00	✓ Complete

PHASE	WEIGHT	PLANNED	ACTUAL	VARIANCE	SPI	STATUS
Z09	1.8%	99.8%	99.2%	-0.6	0.99	▼ Behind
New Scope	1.3%	100.0%	96.4%	-3.6	0.96	▼ Behind
Z13	1.1%	100.0%	100.0%	0.0	1.00	✓ Complete
Z02	1.0%	100.0%	96.7%	-3.3	0.97	▼ Behind
Z03	0.8%	100.0%	100.0%	0.0	1.00	✓ Complete
Z08	0.7%	100.0%	87.3%	-12.7	0.87	▼ Behind
Z04	0.7%	100.0%	92.0%	-8.0	0.92	▼ Behind
Z11	0.7%	100.0%	99.7%	-0.3	1.00	▼ Behind
ELDREES	0.3%	100.0%	100.0%	0.0	1.00	✓ Complete
CCTV	0.0%	100.0%	100.0%	0.0	1.00	✓ Complete
Total	100%	**99.93%**	**99.18%**	**-0.75**	**0.99**	▼ Behind

The P6 schedule statistics (data date 01-Nov-2026) count 9,236 activities: 9,036 completed, 75 in progress and 125 not started, with 50 activities behind. The P6 update finishes the project on 22-Dec-2026 with –87 days of total float.

Scope of work: quantities

Revised BOQ quantity and installed quantity for each network, from the Major Quantities sheet of the 01-Nov-2026 weekly report. "This week" is the change from the 25-Oct-2026 report: the sheet is unchanged, so it is 0 for every item. Every listed item is reported as 100% installed.

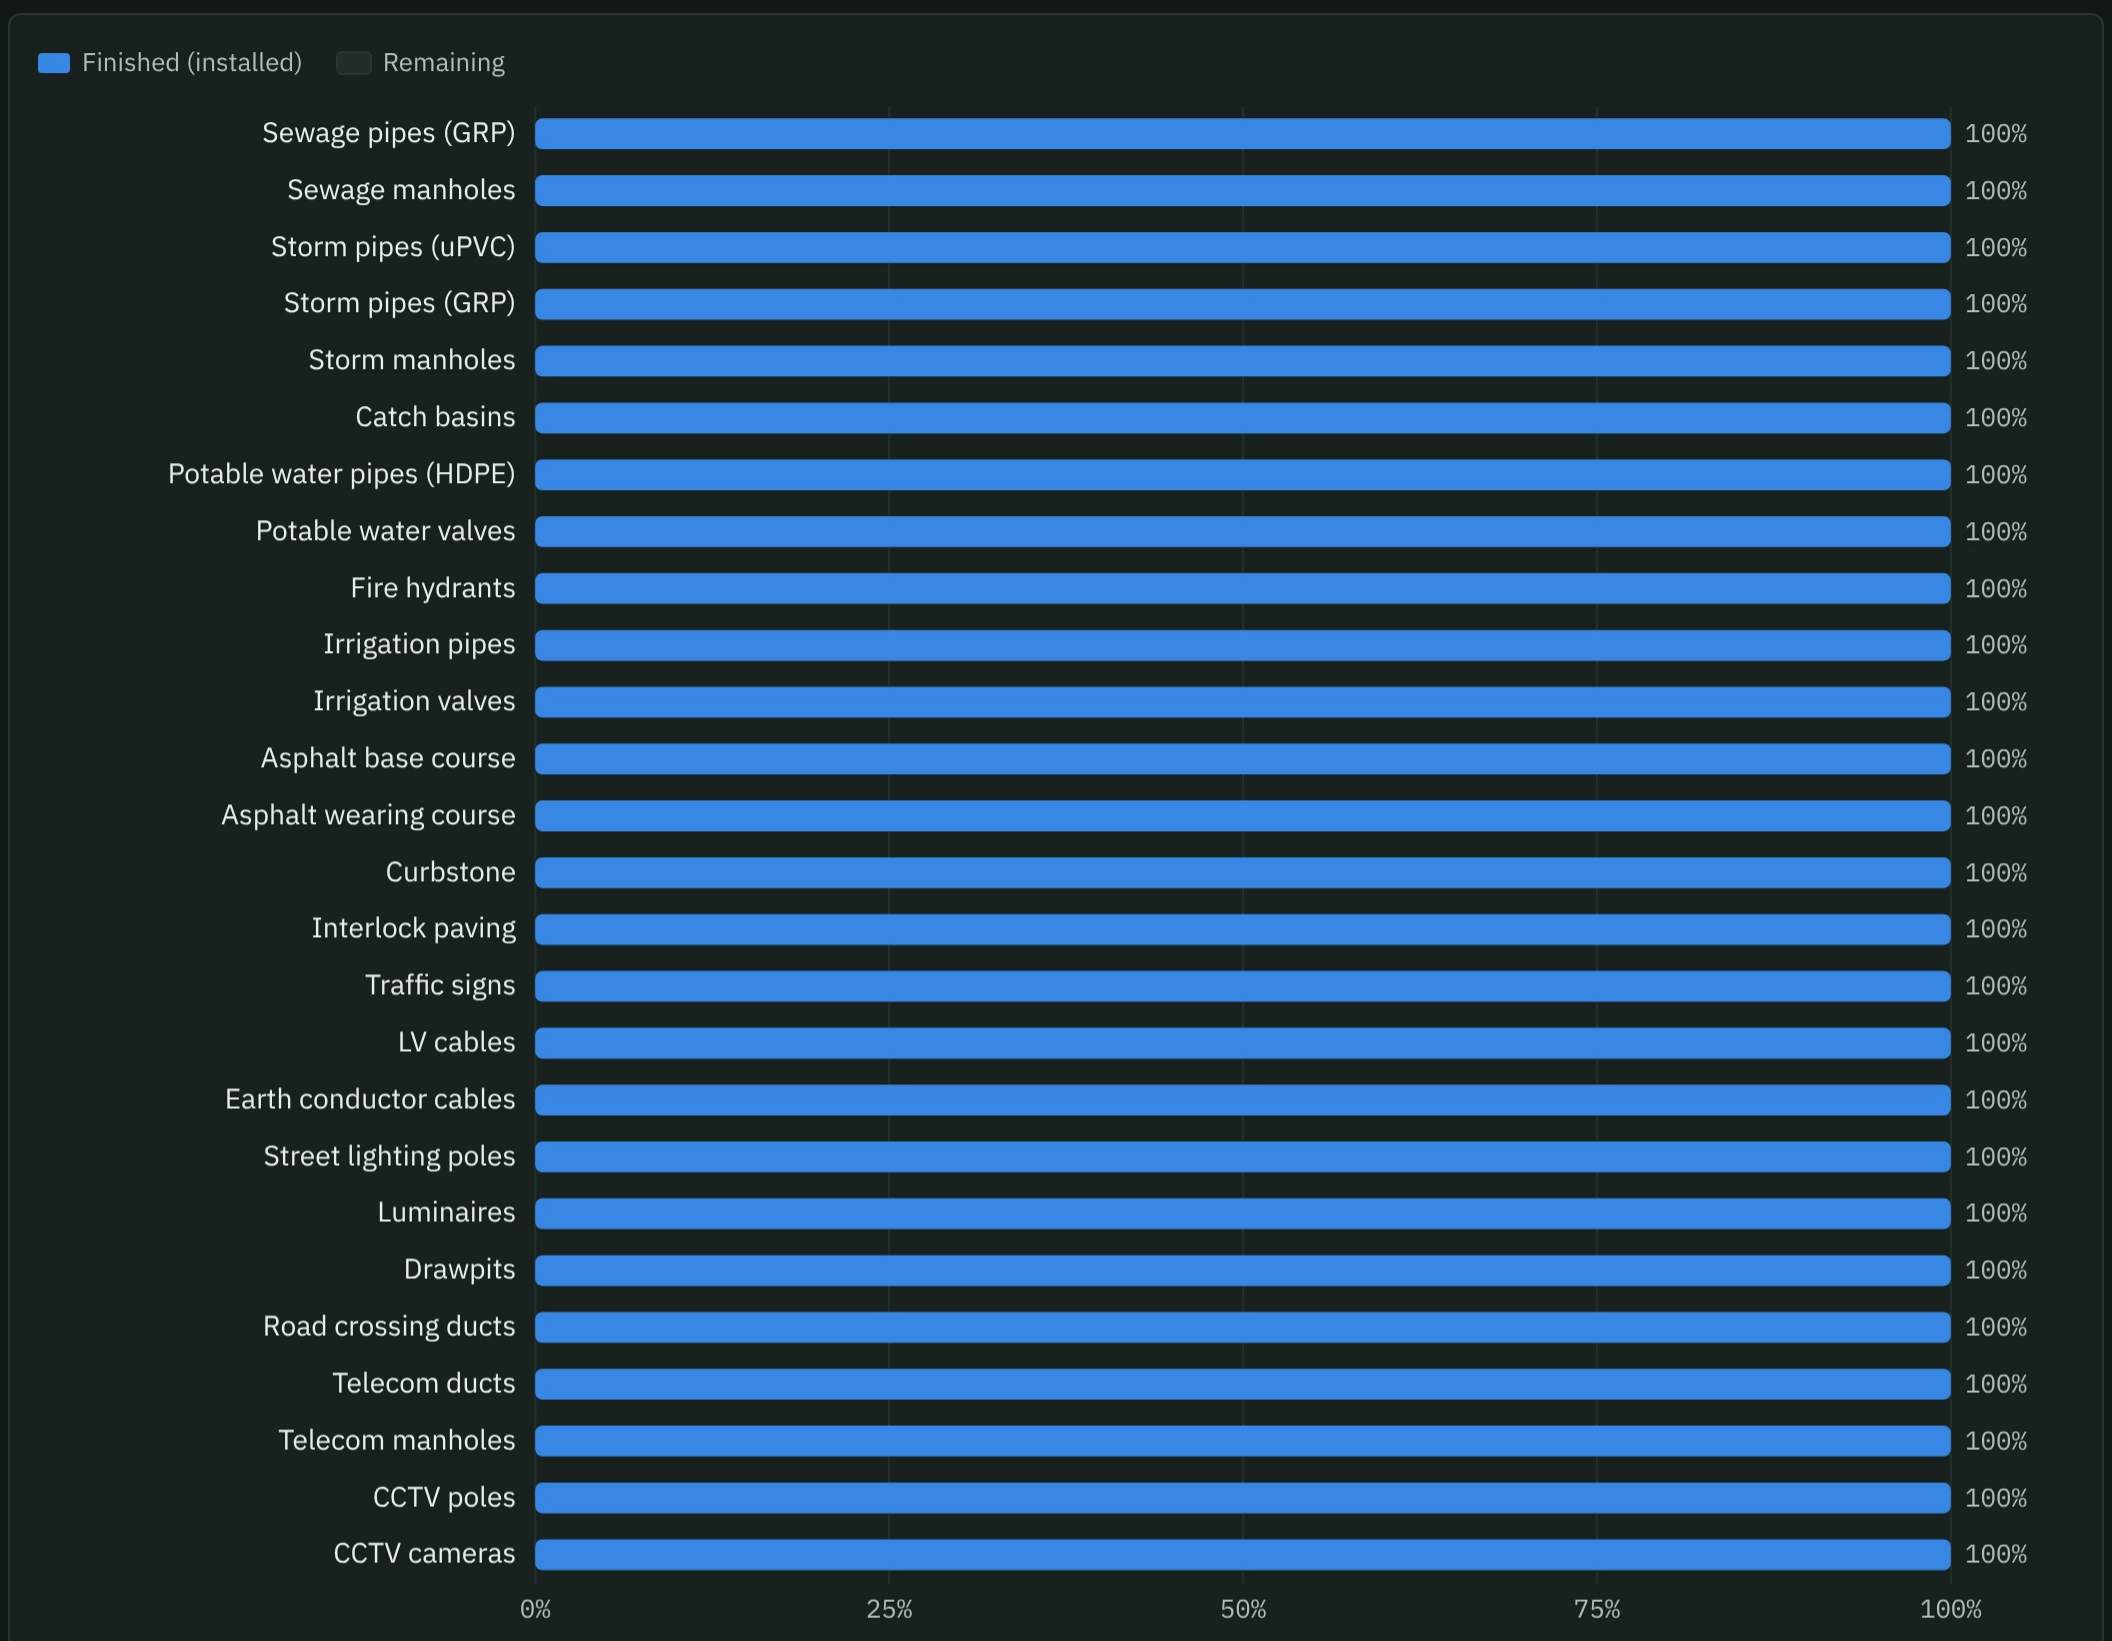

SCOPE ITEM	SIZE / TYPE	UNIT	TOTAL	FINISHED	THIS WEEK	REMAINING	% FINISHED	BACKFILLED
Sewage pipes (GRP)	DN 200	LM	21,379	21,379	0	0	100.0%	–
	DN 250	LM	4,579	4,579	0	0	100.0%	–
	DN 300	LM	204.6	204.6	0	0	100.0%	–
	DN 400	LM	531.9	531.9	0	0	100.0%	–
	Total	LM	**26,695**	**26,695**	**0**	**0**	**100.0%**	–
Sewage manholes	All sizes	EA	355	355	0	0	100.0%	–
Storm pipes (uPVC)	DN 300	LM	29,080	29,080	0	0	100.0%	–
Storm pipes (GRP)	DN 400	LM	11,758	11,758	0	0	100.0%	–
	DN 500	LM	4,240	4,240	0	0	100.0%	–
	DN 600	LM	5,966	5,966	0	0	100.0%	–
	DN 700	LM	5,347	5,347	0	0	100.0%	–

SCOPE ITEM	SIZE / TYPE	UNIT	TOTAL	FINISHED	THIS WEEK	REMAINING	% FINISHED	BACKFILLED
	DN 800	LM	6,312	6,312	0	0	100.0%	–
	DN 900	LM	7,736	7,736	0	0	100.0%	–
	DN 1000	LM	2,856	2,856	0	0	100.0%	–
	DN 1100	LM	1,771	1,771	0	0	100.0%	–
	DN 1200	LM	8,972	8,972	0	0	100.0%	–
	DN 1400	LM	425.4	425.4	0	0	100.0%	–
	Total	LM	**55,383**	**55,383**	**0**	**0**	**100.0%**	–
Storm manholes	DN 1200	EA	203	203	0	0	100.0%	–
	DN 1500	EA	418	418	0	0	100.0%	–
	DN 2000	EA	219	219	0	0	100.0%	–
	Total	EA	**840**	**840**	**0**	**0**	**100.0%**	–
Catch basins	Single	EA	1,007	1,007	0	0	100.0%	–
	Double	EA	761	761	0	0	100.0%	–
	Total	EA	**1,768**	**1,768**	**0**	**0**	**100.0%**	–
Potable water pipes (HDPE)	DN 160	LM	8,045	8,045	0	0	100.0%	–
	DN 225	LM	2,000	2,000	0	0	100.0%	–
	DN 315	LM	215	215	0	0	100.0%	–
	DN 450	LM	1,890	1,890	0	0	100.0%	–
	Total	LM	**12,150**	**12,150**	**0**	**0**	**100.0%**	–
Potable water valves	Gate valves	EA	77	77	0	0	100.0%	–
	Butterfly valves	EA	2	2	0	0	100.0%	–
	Wash-out valves	EA	3	3	0	0	100.0%	–
	Air valves	EA	1	1	0	0	100.0%	–
	Total	EA	**83**	**83**	**0**	**0**	**100.0%**	–
Fire hydrants	ULFM 150	EA	193	193	0	0	100.0%	–
Irrigation pipes	HDPE DN 125	LM	24,479	24,479	0	0	100.0%	–
	HDPE DN 250	LM	28,362	28,362	0	0	100.0%	–
	HDPE DN 315	LM	7,061	7,061	0	0	100.0%	–
	HDPE DN 450	LM	8,870	8,870	0	0	100.0%	–
	HDPE DN 630	LM	2,221	2,221	0	0	100.0%	–
	GRP DN 800	LM	1,340	1,340	0	0	100.0%	–
	Total	LM	**72,333**	**72,333**	**0**	**0**	**100.0%**	–
Irrigation valves	Gate valves	EA	455	455	0	0	100.0%	–
	Butterfly valves	EA	61	61	0	0	100.0%	–
	Wash-out valves	EA	29	29	0	0	100.0%	–
	Air valves	EA	44	44	0	0	100.0%	–
	Total	EA	**589**	**589**	**0**	**0**	**100.0%**	–
Asphalt base course	Grading I	m^3	1,735	1,735	0	0	100.0%	–

SCOPE ITEM	SIZE / TYPE	UNIT	TOTAL	FINISHED	THIS WEEK	REMAINING	% FINISHED	BACKFILLED
Asphalt wearing course	Grading I	m³	1,240	1,240	0	0	100.0%	–
Curbstone	Type K1-D	LM	15,100	15,100	0	0	100.0%	–
	Type L1	LM	1,972	1,972	0	0	100.0%	–
	Depressed K2	LM	750	750	0	0	100.0%	–
	Total	LM	**17,822**	**17,822**	**0**	**0**	**100.0%**	–
Interlock paving	All	m²	1,576	1,576	0	0	100.0%	–
Traffic signs	Single post	EA	31	31	0	0	100.0%	–
	Double post	EA	4	4	0	0	100.0%	–
	Total	EA	**35**	**35**	**0**	**0**	**100.0%**	–
LV cables	4C×6 mm²	LM	1,826	1,826	0	0	100.0%	–
	4C×10 mm²	LM	2,092	2,092	0	0	100.0%	–
	4C×16 mm²	LM	896	896	0	0	100.0%	–
	4C×25 mm²	LM	7,396	7,396	0	0	100.0%	–
	4C×35 mm²	LM	11,757	11,757	0	0	100.0%	–
	4C×50 mm²	LM	120	120	0	0	100.0%	–
	4C×150 mm²	LM	1,500	1,500	0	0	100.0%	–
	Total	LM	**25,587**	**25,587**	**0**	**0**	**100.0%**	–
Earth conductor cables	6 mm²	LM	4,208	4,208	0	0	100.0%	–
	16 mm²	LM	20,049	20,049	0	0	100.0%	–
	70 mm²	LM	2,700	2,700	0	0	100.0%	–
	Total	LM	**26,957**	**26,957**	**0**	**0**	**100.0%**	–
Street lighting poles	12 m, 2 arms	EA	10	10	0	0	100.0%	–
	12 m, 1 arm	EA	220	220	0	0	100.0%	–
	Total	EA	**230**	**230**	**0**	**0**	**100.0%**	–
Luminaires	LED 150 W	EA	240	240	0	0	100.0%	–
	LED 342 W	EA	88	88	0	0	100.0%	–
	LED 208 W	EA	102	102	0	0	100.0%	–
	Total	EA	**430**	**430**	**0**	**0**	**100.0%**	–
Drawpits	600×600	EA	783	783	0	0	100.0%	–
	900×900	EA	151	151	0	0	100.0%	–
	900×1800	EA	18	18	0	0	100.0%	–
	Total	EA	**952**	**952**	**0**	**0**	**100.0%**	–
Road crossing ducts	UPVC 160 mm	LM	1,116	1,116	0	0	100.0%	–
Telecom ducts	6-way, 50 mm	LM	8,100	8,100	0	0	100.0%	–
Telecom manholes	Type 1	EA	90	90	0	0	100.0%	–
CCTV poles	All	EA	18	18	0	0	100.0%	–
CCTV cameras	All	EA	82	82	0	0	100.0%	–

Revised quantities are far below the original BOQ for roads

The revised BOQ, still marked "under review", sets each total equal to the installed quantity. For road works it is a small part of the original BOQ: asphalt wearing course 1,240 of 63,689 m³, precast kerb K1-D 15,100 of 187,209 m, kerb L1 1,972 of 123,805 m and interlock 1,576 of 59,537 m².

The sheet conflicts with the remaining-activities list

The P6 update of 01-Nov-2026 still has the storm network open in zones Z04, Z05, Z08 and Z11 (finishing 16 to 24-Nov-2026) and Main Roads and Z02 finishing on 05 and 07-Nov-2026. Last week's remaining-activities list showed uPVC 300 mm and GRP 400 mm catch-basin lines still to lay in these zones. The quantities above therefore overstate what is installed.

Medium-voltage works revised to zero

The 13.8 kV cable (30,720 m in the original BOQ), its joints and terminations, the 950 m duct bank, the normally-open RMUs and the three street-lighting substations and RMUs all have a revised quantity of 0. They are left out of the table.

Milestones

Baseline and weekly-report dates from the Milestones sheet; P6 forecasts and total float from the P6 schedule update (XER, data date 01-Nov-2026, 10-hour days). The two sources disagree, so both are shown.


MILESTONE	BASELINE	WEEKLY REPORT FORECAST	P6 UPDATE FORECAST	P6 FLOAT (DAYS)	STATUS
Site handover	29-Jul-2024	29-Jul-2024 (actual)	29-Jul-2024 (actual)	–	✓ Done
Complete mobilisation	03-Sep-2024	26-Oct-2024 (actual)	11-Dec-2024 (actual)	–	✓ Done
Existing-condition survey and final reports	07-Sep-2025	23-Jul-2025 (actual)	01-Nov-2026	−31	? Conflicts with P6
Complete mechanical works	01-Oct-2025	27-Jun-2026	05-Nov-2026	−34	▼ Late
Complete steel structure erection	02-Jul-2026	25-Feb-2026	01-Nov-2026	−31	▼ Late
Complete earthworks	07-Jul-2026	02-Jul-2026	01-Nov-2026	−31	▼ Late
Complete all civil works	07-Jul-2026	02-Jul-2026	01-Nov-2026	−31	▼ Late
Complete demobilisation	23-Jul-2026	20-Jul-2026	01-Nov-2026	−31	▼ Late
Finish road kerbing and pavement	28-Jun-2026	–	01-Nov-2026	−31	▼ Late
Finish water networks (potable and TSE)	12-Sep-2026	–	02-Nov-2026	−31	▼ Late
Approval of all as-built drawings	–	–	08-Nov-2026	−37	▼ Late
Finish sewage, storm and electrical networks	26-Sep-2026	–	24-Nov-2026	−51	▼ Late
All works complete, ready for initial handover	28-Jul-2026	28-Jul-2026	24-Nov-2026	−51	▼ Late
Construction (P6)	26-Sep-2026	–	24-Nov-2026	−59	▼ Late
Close-out (P6)	26-Sep-2026	–	22-Dec-2026	−75	▼ Late
Project completion	26-Sep-2026 (original 28-Jul-2026)	30-Nov-2026 (+65 d)	22-Dec-2026	−87	▼ Late

The two completion forecasts are 22 days apart, and six milestones are forecast on the data date itself.

The weekly report forecasts completion on 30-Nov-2026; the P6 update finishes on 22-Dec-2026. Six milestones, including earthworks, civil works, demobilisation and road kerbing, are forecast on 01-Nov-2026, the data date: they are not finished and move forward with each update (last week they were forecast for 25 to 28-Oct-2026). The milestone sheet of the weekly report still gives forecast dates between February and July 2026.

Procurement of key materials

Delivered quantity against the revised BOQ quantity. Source: Major Quantities sheet, weekly report 18-Oct-2026.

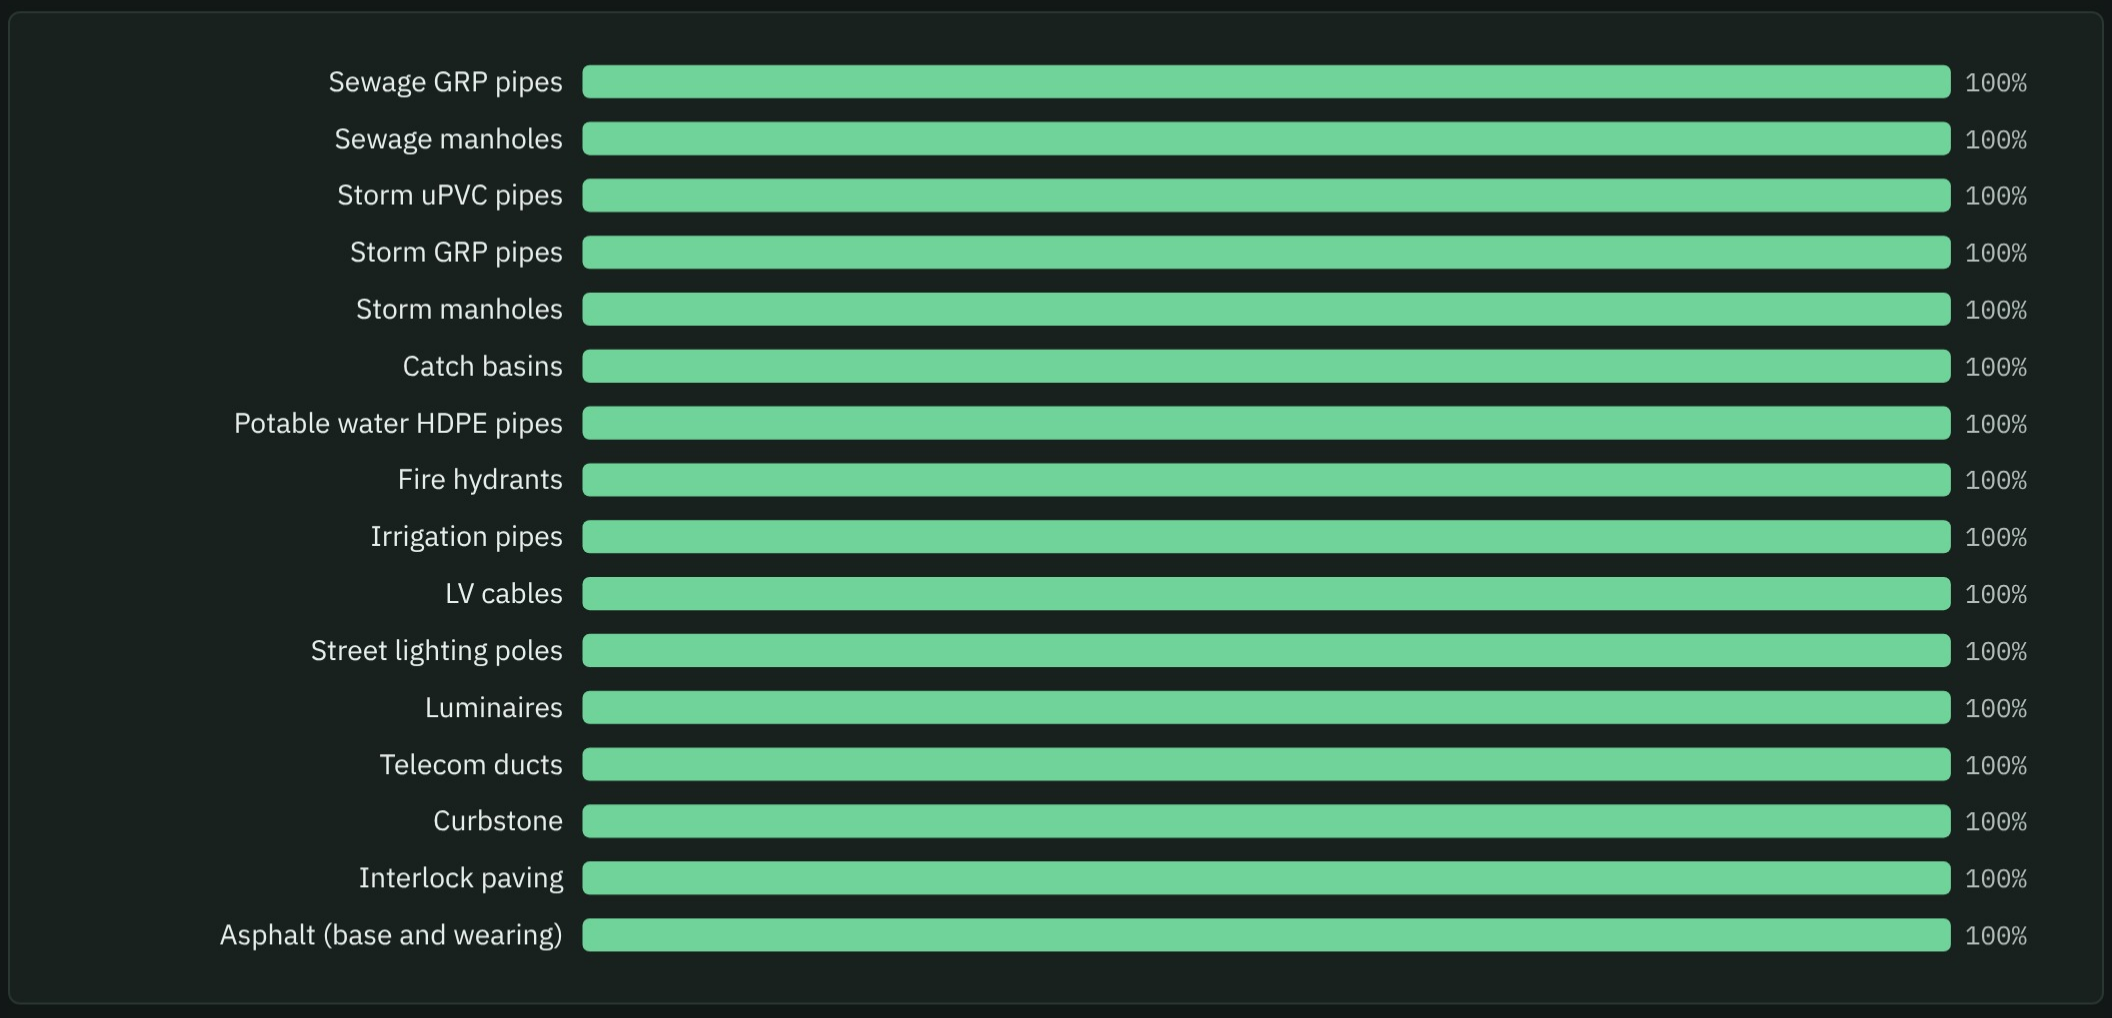

Deliveries complete against the revised quantities


Every material in the Major Quantities sheet is 100% delivered and installed against its revised quantity. The procurement summary still shows 12 of 20 purchase orders issued, 8 remaining and 10 materials on site.

The Procurement sheet is out of date

The detailed Procurement sheet, hidden in the workbook, still gives delivery rates from an earlier stage, for example kerbs 4.8%, interlock 6.9% and fire hydrants 79%. Nine of its 42 items are marked "to be descoped".

Manpower

Monthly manual head count, planned vs actual, August 2024 to January 2026, the last month with an actual figure. Source: Manpower sheet.

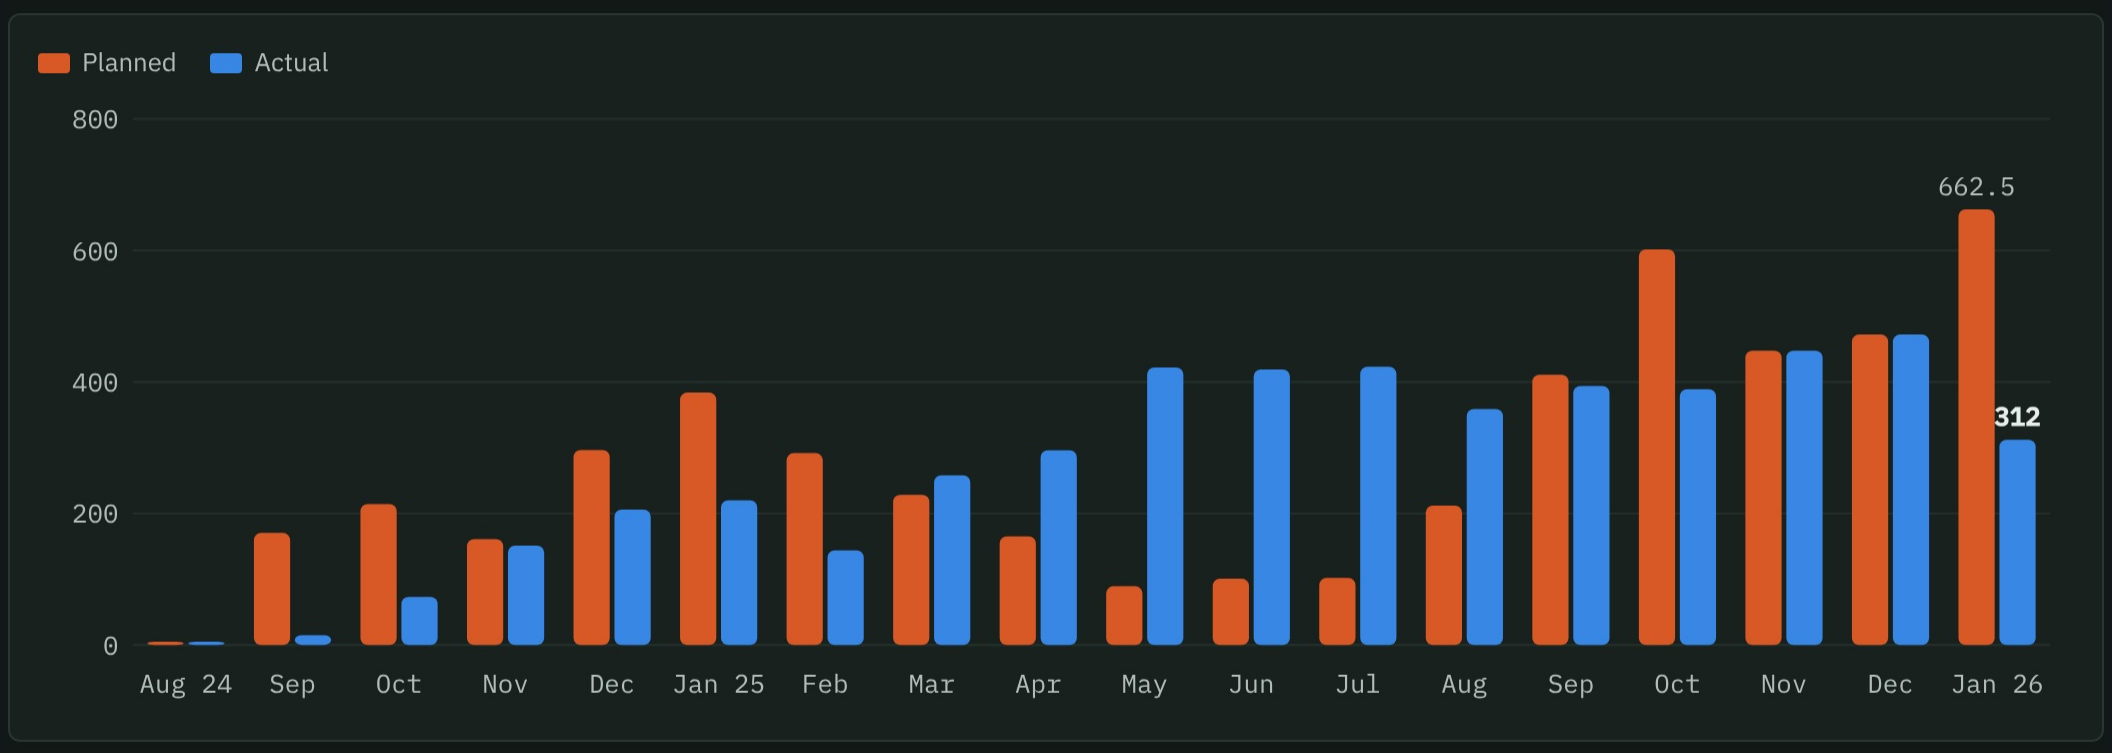

January 2026: 312 against 662.5 planned. The November and December 2025 actuals are identical to the planned values. For October 2026 the resources panel reports 1,092 manual and 92 non-manual staff for the third week running, with no plan for the month. The trade breakdown lists 389 workers against 602 planned. Equipment on site: 135 against 167 planned, 3 idle.

Cost and invoicing

Contract value

Storm water network	161,546,482
Roads, paving, markings and signage	67,012,837
TSE (irrigation) network	49,057,170
Industrial sewage network	19,706,041
Electrical works	13,120,144
Potable water network	9,302,202
BOQ total (excl. VAT)	**319,744,876**
Contract value incl. 15% VAT	367,706,607
Change orders	2 (no cost)

All values in SAR. CCO 1 (revised BOQ, approved 23-Jul-2025) and CCO 2 (two-month extension of time, approved 29-Jun-2026) do not change the contract value.

Invoices

Invoices submitted	25
Gross value	268,762,557
Advance payment recovery	26,876,256
Deductions and penalties	260,000
Retention	0
Net incl. VAT	277,909,247
PM-approved (24 invoices)	258,711,628
Paid (recorded)	0
FIR value to date	278,910,229

Invoicing is 84.1% of the contract value against 99.18% physical progress. Invoice #25 (period to 26-Sep-2026, gross 18,548,424) was submitted and approved by the consultant on 01-Nov-2026. The log records no payments.

Health, safety and quality

Safety Score 0.86

Safe man-hours (cumulative)	2,383,300
Man-hours this week	15,300
Lost-time injuries	0
Fatalities	0
First-aid cases	0
Near misses (cumulative)	11
Vehicle incidents (cumulative)	1
Inductions / toolbox talks	227 / 3,410

HSE site inspection of 01-Nov-2026. This week: 10 toolbox talks and 3 internal trainings.

Quality Score 0.91

NCRs issued / closed / open	148 / 138 / 10
Site instructions issued / open	187 / 1
MIRs issued / open	357 / 2
FIRs issued / pending	32,177 / 791
RFIs issued / closed	239 / 239
Shop drawings submitted / total	2,532 / 2,551
Material submittals pending	35 of 78
As-built drawings submitted / approved (A) / total	655 / 530 / 980

QC inspection 01-Nov-2026. This week 8 NCRs were issued and 9 closed, and pending FIRs rose from 435 to 791. As-built figures are from the As-Built Tracker of 25-Oct-2026; no newer tracker was uploaded.

Open issues and risks

ISSUE	OWNER	DETAIL
As-built drawings	MODON	The as-built drawings do not match site conditions, so connection areas need excavation to locate services.
Utility corridor cross-sections	MODON	The cross-section in the contract documents does not match the site; each road needs its own approved cross-section.
Factory inside the work area	MODON	A factory lies within the work area, so the networks on these roads must be re-routed. No official consultant response yet.
Existing lines change the scope	MODON	Existing lines found by the survey change the network layout and reduce the scope, as happened with the industrial sewage and water networks.
Existing MV lines	MODON	Existing MV lines change the scope, and MV as-built data has not been given to the contractor.
Box culvert, Zone 01	Contractor	More existing utilities than expected; the work continues slowly and carefully.
Box culvert, Zone 06	MODON	The excavation conflicts with a factory and its entrance.

All open items in the issue log were raised between September and December 2024 and are still marked Active; the log has no newer entries. Not in the log: as-built drawings were 54% approved (530 of 980) on 25-Oct-2026, while P6 now plans all approvals by 08-Nov-2026 (–37 days).

Data notes

- Week number: the Milestones sheet states contract week 118 ("118 of 103"), which is used. This also confirms the 117 used for last week's report, when the cell showed an error.
- Major Quantities is unchanged since 18-Oct-2026 and shows every item 100% installed, while the P6 update still has the storm network open in four zones until 16 to 24-Nov-2026.
- The Physical-Chart Data sheet was corrected this week: actual progress at the end of July, August and September is now 77.2%, 81.8% and 95.8% (previously 79.3%, 85.1% and 100%). The sheet now states percentages against 48,012 man-hours (99.25% for October); this report uses the 48,045 budget of the Progress sheet (99.18%).
- The weekly report moved its completion forecast from 15-Nov to 30-Nov-2026, while P6 gives 22-Dec-2026. Six P6 milestones are forecast on the data date, and the weekly report gives the existing-condition survey as finished in July 2025 while P6 still has it open.
- The Progress Tracking Sheet (.xlsb) shows catch-basin pipes 19,242 of 38,652 m, catch basins 959 of 1,902 and sewer pipes 25,494 of 27,859 m installed, and its targets are for January 2026. It conflicts with both the weekly report and P6 and appears out of date, so it was not used.
- No site photos this week: the only photos are the June 2025 ones in the hidden Weekly Photos sheet, and the PDFs contain drawings only. The Progress Layouts are still dated 09-Aug-2026, the As-Built Progress Layouts are colour-coded maps without counts, and the Procurement Tracker is still dated 23-Aug-2026.
- Manpower: the October head count (1,092 manual, 92 non-manual) is repeated for the third week and does not match the trade breakdown (389); monthly actuals stop at January 2026.
- The invoice summary shows 0 submitted invoices while the log lists 25. The Testing sheet still shows 0% for all systems, while P6 has testing and commissioning in progress.
- The workbook also reports cost-based progress (value-weighted) and labels it as planned and actual. This report uses physical % complete (man-hour weighted) only.

Compiled 08-Nov-2026 from the weekly report and P6 update with data date 01-Nov-2026 and, for this-week values, the report of 25-Oct-2026.
