
Infrastructure Works of Area J -3rd Industrial City-Dammam-Phase 2 - Part 2 Update 06/10/2026

WPR UPS LEVEL 5

Activity ID	Activity Name	Original Duration	BL Project Start	BL Project Finish	Start	Finish	BL Project Total Cost	Earned Value Cost	Schedule % Complete	Performance % Complete
Infrastructure Works of Area J -3rd Industrial City-Dammam-Phase 2 - F		856	12-Jan-25	11-Jan-27	12-Jan-25 A	08-Nov-27	117,391,774.00	86,689,746.16	82.48%	73.85%
Key Milestones		856	12-Jan-25	11-Jan-27	12-Jan-25 A	08-Nov-27	0.00	0.00	0%	0%
Contractual Milestones		856	12-Jan-25	11-Jan-27	12-Jan-25 A	08-Nov-27	0.00	0.00	0%	0%
MS-CF-IR	Completion of Construction Works for Irrigation Network	0		28-Oct-26		13-Jul-27*	0.00	0.00	0%	0%
MS-CF-MV	Completion of Construction Works for Medium Voltage Network	0		28-Oct-26		21-Aug-27*	0.00	0.00	0%	0%
MS-CF-PW	Completion of Construction Works for Potable Water Network	0		18-Nov-26		30-Aug-27*	0.00	0.00	0%	0%
MS-CF-RD	Completion of Construction Works for Road Works	0		28-Dec-26		25-Oct-27	0.00	0.00	0%	0%
MS-CF-SW	Completion of Construction Works for Sewage Network	0		08-Nov-26		03-Aug-27*	0.00	0.00	0%	0%
MS-CF-SD	Completion of Construction Works for Storm Drainage Network	0		12-Dec-26		23-Aug-27*	0.00	0.00	0%	0%
MS-CF-SL	Completion of Construction Works for Street Lighting Network	0		15-Oct-26		11-Sep-27*	0.00	0.00	0%	0%
MS-CF-TE	Completion of Construction Works for Telecom Network	0		01-Sep-26		28-Apr-27*	0.00	0.00	100%	0%
MS-CF-MOB	Completion of Mobilization Works	0		09-Mar-25		09-Mar-25 A	0.00	0.00	100%	100%
MS-CF-ENG	Completion of Submitting and Approval of Shopdrwing and Material	0		10-Feb-25		24-May-25 A	0.00	0.00	100%	100%
MS-CF-EBL	Completion of Work Plan and Baseline Schedule	0		10-Feb-25		10-Mar-25 A	0.00	0.00	100%	100%
MS-CS-PS	Project Commencement Date (Site Handover)	0	12-Jan-25		12-Jan-25 A		0.00	0.00	100%	100%
MS-CF-PF	Project Completion Date	0		11-Jan-27		08-Nov-27	0.00	0.00	0%	0%
Control Milestones		359	09-Jul-25	21-Jun-26	29-Apr-25 A	06-Oct-26	0.00	0.00	0%	0%
MS-CS-IR	The Employer Approval NOC for Irrigation Network	0	19-Nov-25		16-Jun-25 A		0.00	0.00	100%	100%
MS-CS-MV	The Employer Approval NOC for Medium Voltage Network	0	14-Feb-26		06-Oct-26		0.00	0.00	100%	0%
MS-CS-PW	The Employer Approval NOC for Potable Water Network	0	03-Nov-25		19-Jun-25 A		0.00	0.00	100%	100%
MS-CS-RD	The Employer Approval NOC for Roads Works	0	21-Jun-26		10-Jul-25 A		0.00	0.00	100%	100%
MS-CS-SW	The Employer Approval NOC for Sewage Network	0	09-Jul-25		29-Apr-25 A		0.00	0.00	100%	100%
MS-CS-SD	The Employer Approval NOC for Storm Drainage Network	0	08-Sep-25		30-Apr-25 A		0.00	0.00	100%	100%
MS-CS-SL	The Employer Approval NOC for Street Lighting Network	0	29-Dec-25		08-Jul-25 A		0.00	0.00	100%	100%
MS-CS-TE	The Employer Approval NOC for Telecom Network	0	03-May-26		08-Jul-25 A		0.00	0.00	100%	100%
Intermediate Milestones		78	24-Aug-26	28-Dec-26	25-Jul-27	25-Oct-27	0.00	0.00	0%	0%
MS-MO-10	Completion of Sewage Pump Stations	0		01-Dec-26		25-Jul-27	0.00	0.00	0%	0%
MS-MO-30	Completion of Tie In To Existing Networks	0		28-Dec-26		25-Oct-27	0.00	0.00	0%	0%
MS-MO-20	Completion of Storm Drainage Ponds	0		24-Aug-26		04-Aug-27	0.00	0.00	100%	0%
Preliminaries and Mobilization Works		48	12-Jan-25	09-Mar-25	12-Jan-25 A	12-Mar-25 A	0.00	0.00	0%	0%
Mobilization Works		48	12-Jan-25	09-Mar-25	12-Jan-25 A	12-Mar-25 A	0.00	0.00	0%	0%
MOB-10	Clear and Grub for Offices and Access Roads	24	12-Jan-25	08-Feb-25	12-Jan-25 A	12-Mar-25 A	0.00	0.00	100%	100%
MOB-40	Construction Project Store & Temporary Fence	24	09-Feb-25	09-Mar-25	09-Feb-25 A	12-Mar-25 A	0.00	0.00	100%	100%
MOB-80	Construction Site Access Roads	24	09-Feb-25	09-Mar-25	09-Feb-25 A	12-Mar-25 A	0.00	0.00	100%	100%
MOB-70	Installation Project Sign Board	24	09-Feb-25	09-Mar-25	09-Feb-25 A	12-Mar-25 A	0.00	0.00	100%	100%
MOB-60	Mobilization of Major Equipments	24	09-Feb-25	09-Mar-25	09-Feb-25 A	12-Mar-25 A	0.00	0.00	100%	100%
MOB-50	Mobilization of Major Manpower	24	09-Feb-25	09-Mar-25	09-Feb-25 A	12-Mar-25 A	0.00	0.00	100%	100%

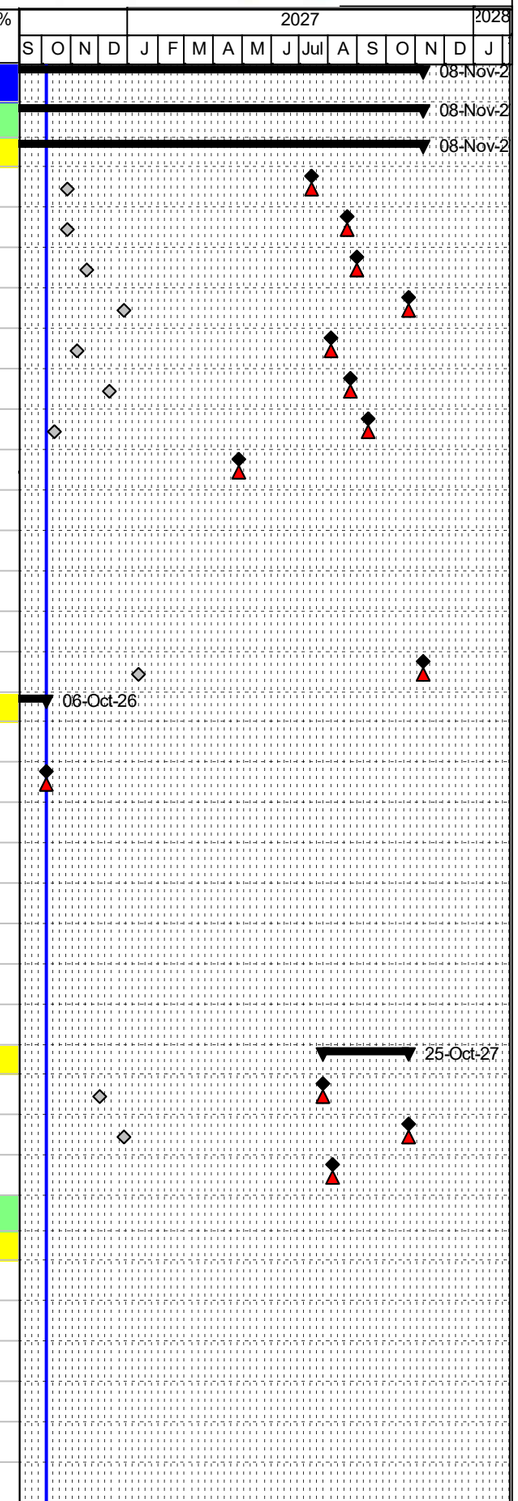


Primary Baseline | Actual Work | Summary

Remaining Work | Baseline Milestone

Critical Remaining Work | Milestone

Date	Revision	Checked	Approved
06-Oct-26	Third Industrial City		


Activity ID	Activity Name	Original Duration	BL Project Start	BL Project Finish	Start	Finish	BL Project Total Cost	Earned Value Cost	Schedule % Complete	Performance % Complete
MOB-20	Project Site Layout Plan Approval	24	12-Jan-25	08-Feb-25	12-Jan-25 A	12-Mar-25 A	0.00	0.00	100%	100%
MOB-30	Supply & Install of Project Supervision Offices	24	09-Feb-25	09-Mar-25	09-Feb-25 A	12-Mar-25 A	0.00	0.00	100%	100%
Project Documents Provision From The Employer		0	12-Jan-25	12-Jan-25	12-Jan-25 A	12-Feb-25 A	0.00	0.00	0%	0%
PRE-EMP-MDC-1	Receive of Approved Project Master Plans of works (IFC) From The Employer	0	12-Jan-25		12-Jan-25 A		0.00	0.00	100%	100%
PRE-EMP-MDC-2	Receive of Site Benchmark Coordinates (Original Point) From The Employer	0	12-Jan-25		12-Feb-25 A		0.00	0.00	100%	100%
PRE-EMP-MDC-3	Receive of Site Surveying Details From The Employer	0	12-Jan-25		12-Feb-25 A		0.00	0.00	100%	100%
Project Main Documents From The Contractor		26	12-Jan-25	10-Feb-25	12-Jan-25 A	02-Mar-25 A	0.00	0.00	0%	0%
PRE-CON-MDC-2	Submission Project Baseline Schedule	26	12-Jan-25	10-Feb-25	12-Jan-25 A	01-Mar-25 A	0.00	0.00	100%	100%
PRE-CON-MDC-7	Submission Project Environmental Plan	26	12-Jan-25	10-Feb-25	12-Jan-25 A	02-Mar-25 A	0.00	0.00	100%	100%
PRE-CON-MDC-6	Submission Project Geotechnical Soil Report	26	12-Jan-25	10-Feb-25	12-Jan-25 A	02-Mar-25 A	0.00	0.00	100%	100%
PRE-CON-MDC-3	Submission Project Health & Safety Plan	26	12-Jan-25	10-Feb-25	12-Jan-25 A	02-Mar-25 A	0.00	0.00	100%	100%
PRE-CON-MDC-8	Submission Project Organization Chart and Communications Plan	26	12-Jan-25	10-Feb-25	12-Jan-25 A	02-Mar-25 A	0.00	0.00	100%	100%
PRE-CON-MDC-4	Submission Project Quality Control Plan	26	12-Jan-25	10-Feb-25	12-Jan-25 A	02-Mar-25 A	0.00	0.00	100%	100%
PRE-CON-MDC-5	Submission Project Surveying Report	26	12-Jan-25	10-Feb-25	12-Jan-25 A	02-Mar-25 A	0.00	0.00	100%	100%
Engineering Works		165	12-Jan-25	16-Feb-25	12-Jan-25 A	02-Jun-25 A	3,015,066.97	3,015,066.97	100%	100%
Design Reviews		9	12-Jan-25	21-Jan-25	12-Jan-25 A	21-Jan-25 A	0.00	0.00	0%	0%
Infrastructure Networks		9	12-Jan-25	21-Jan-25	12-Jan-25 A	21-Jan-25 A	0.00	0.00	0%	0%
Road Works		9	12-Jan-25	21-Jan-25	12-Jan-25 A	21-Jan-25 A	0.00	0.00	0%	0%
Sewage Network		9	12-Jan-25	21-Jan-25	12-Jan-25 A	21-Jan-25 A	0.00	0.00	0%	0%
Storm Drainage Network		9	12-Jan-25	21-Jan-25	12-Jan-25 A	21-Jan-25 A	0.00	0.00	0%	0%
Potable Water Network		9	12-Jan-25	21-Jan-25	12-Jan-25 A	21-Jan-25 A	0.00	0.00	0%	0%
Irrigation Network		9	12-Jan-25	21-Jan-25	12-Jan-25 A	21-Jan-25 A	0.00	0.00	0%	0%
Medium Voltage Network		9	12-Jan-25	21-Jan-25	12-Jan-25 A	21-Jan-25 A	0.00	0.00	0%	0%
Street Lighting Network		9	12-Jan-25	21-Jan-25	12-Jan-25 A	21-Jan-25 A	0.00	0.00	0%	0%
Telecom Network		9	12-Jan-25	21-Jan-25	12-Jan-25 A	21-Jan-25 A	0.00	0.00	0%	0%
Superstructure Works		9	12-Jan-25	21-Jan-25	12-Jan-25 A	21-Jan-25 A	0.00	0.00	0%	0%
Sewage Pump Stations (PS06)		9	12-Jan-25	21-Jan-25	12-Jan-25 A	21-Jan-25 A	0.00	0.00	0%	0%
Storm Drainage Ponds (PO-J1 , PO-J2)		9	12-Jan-25	21-Jan-25	12-Jan-25 A	21-Jan-25 A	0.00	0.00	0%	0%
Shop Drawings		17	22-Jan-25	10-Feb-25	22-Jan-25 A	19-May-25 A	0.00	0.00	0%	0%
Infrastructure Networks		17	22-Jan-25	10-Feb-25	22-Jan-25 A	19-May-25 A	0.00	0.00	0%	0%
Road Works		17	22-Jan-25	10-Feb-25	22-Jan-25 A	19-May-25 A	0.00	0.00	0%	0%
Sewage Network		12	22-Jan-25	04-Feb-25	22-Jan-25 A	28-Apr-25 A	0.00	0.00	0%	0%
Storm Drainage Network		16	22-Jan-25	09-Feb-25	22-Jan-25 A	09-Feb-25 A	0.00	0.00	0%	0%
Potable Water Network		15	22-Jan-25	08-Feb-25	22-Jan-25 A	13-May-25 A	0.00	0.00	0%	0%
Irrigation Network		16	22-Jan-25	09-Feb-25	22-Jan-25 A	28-Apr-25 A	0.00	0.00	0%	0%
Medium Voltage Network		16	22-Jan-25	09-Feb-25	22-Jan-25 A	09-Feb-25 A	0.00	0.00	0%	0%
Street Lighting Network		16	22-Jan-25	09-Feb-25	22-Jan-25 A	09-Feb-25 A	0.00	0.00	0%	0%
Telecom Network		16	22-Jan-25	09-Feb-25	22-Jan-25 A	09-Feb-25 A	0.00	0.00	0%	0%
Superstructure Works		17	22-Jan-25	10-Feb-25	22-Jan-25 A	10-Feb-25 A	0.00	0.00	0%	0%
Sewage Pump Stations (PS 06)		17	22-Jan-25	10-Feb-25	22-Jan-25 A	10-Feb-25 A	0.00	0.00	0%	0%
Storm Drainage Ponds (PO-J1 , PO-J2)		17	22-Jan-25	10-Feb-25	22-Jan-25 A	10-Feb-25 A	0.00	0.00	0%	0%
Method Statements		17	22-Jan-25	10-Feb-25	22-Jan-25 A	10-Feb-25 A	0.00	0.00	0%	0%
Infrastructure Networks		17	22-Jan-25	10-Feb-25	22-Jan-25 A	10-Feb-25 A	0.00	0.00	0%	0%
Road Works		17	22-Jan-25	10-Feb-25	22-Jan-25 A	10-Feb-25 A	0.00	0.00	0%	0%
Sewage Network		12	22-Jan-25	04-Feb-25	22-Jan-25 A	08-Feb-25 A	0.00	0.00	0%	0%
Storm Drainage Network		16	22-Jan-25	09-Feb-25	22-Jan-25 A	09-Feb-25 A	0.00	0.00	0%	0%
Potable Water Network		15	22-Jan-25	08-Feb-25	22-Jan-25 A	08-Feb-25 A	0.00	0.00	0%	0%
Irrigation Network		16	22-Jan-25	09-Feb-25	22-Jan-25 A	09-Feb-25 A	0.00	0.00	0%	0%
Medium Voltage Network		16	22-Jan-25	09-Feb-25	22-Jan-25 A	09-Feb-25 A	0.00	0.00	0%	0%

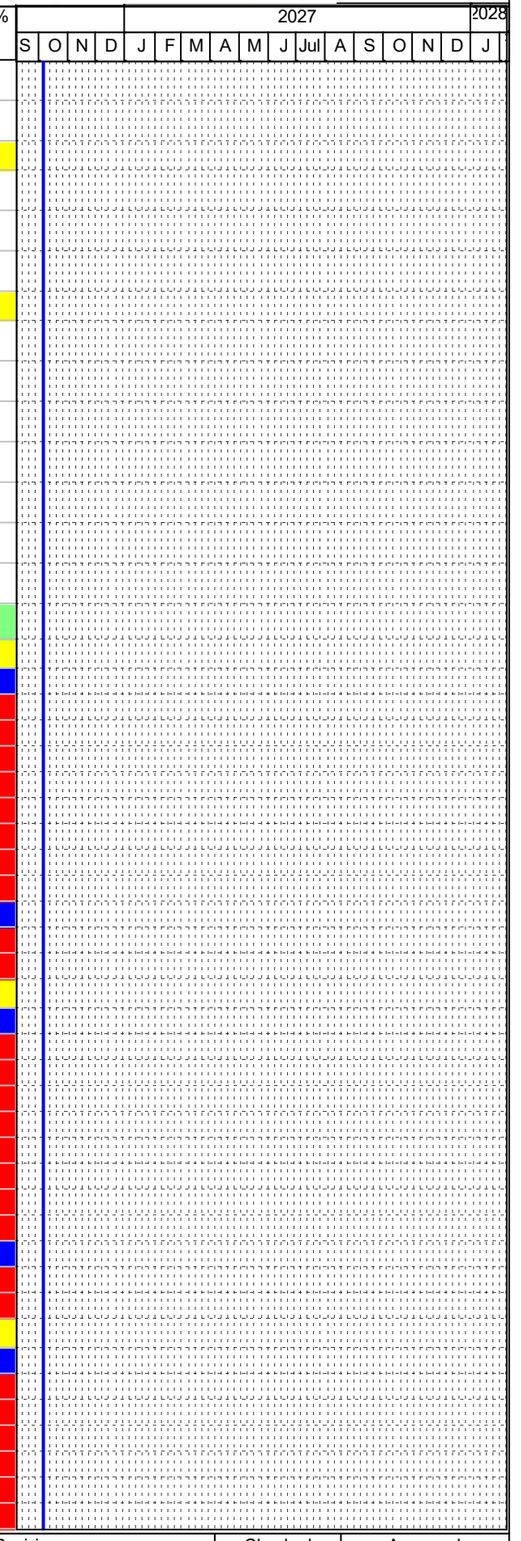

Primary Baseline | Actual Work | Summary
Remaining Work | Baseline Milestone
Critical Remaining Work | Milestone

Date	Revision	Checked	Approved
06-Oct-26	Third Industrial City		

Activity ID	Activity Name	Original Duration	BL Project Start	BL Project Finish	Start	Finish	BL Project Total Cost	Earned Value Cost	Schedule % Complete	Performance % Complete
	Street Lighting Network	16	22-Jan-25	09-Feb-25	22-Jan-25 A	09-Feb-25 A	0.00	0.00	0%	0%
	Telecom Network	16	22-Jan-25	09-Feb-25	22-Jan-25 A	09-Feb-25 A	0.00	0.00	0%	0%
	Superstructure Works	17	22-Jan-25	10-Feb-25	22-Jan-25 A	10-Feb-25 A	0.00	0.00	0%	0%
	Sewage Pump Stations (PS 06)	17	22-Jan-25	10-Feb-25	22-Jan-25 A	10-Feb-25 A	0.00	0.00	0%	0%
	Storm Drainage Ponds (PO-J1 , PO-J2)	17	22-Jan-25	10-Feb-25	22-Jan-25 A	10-Feb-25 A	0.00	0.00	0%	0%
	Material Submittals	156	22-Jan-25	16-Feb-25	22-Jan-25 A	02-Jun-25 A	3,015,066.97	3,015,066.97	100%	100%
	Short Lead Time Items	156	22-Jan-25	16-Feb-25	22-Jan-25 A	01-Jun-25 A	2,848,900.57	2,848,900.57	100%	100%
	Infrastructure Networks	156	22-Jan-25	16-Feb-25	22-Jan-25 A	01-Jun-25 A	2,736,286.15	2,736,286.15	100%	100%
	Superstructure Works	17	22-Jan-25	10-Feb-25	22-Jan-25 A	11-May-25 A	112,614.42	112,614.42	100%	100%
	Long Lead Time Items	57	22-Jan-25	10-Feb-25	01-Feb-25 A	02-Jun-25 A	166,166.40	166,166.40	100%	100%
	Infrastructure Networks	7	22-Jan-25	30-Jan-25	01-Feb-25 A	23-May-25 A	10,780.80	10,780.80	100%	100%
	Superstructure Works	17	22-Jan-25	10-Feb-25	11-May-25 A	02-Jun-25 A	155,385.60	155,385.60	100%	100%
	Procurement Cycle	743	05-Feb-25	05-Oct-26	11-Feb-25 A	22-Jul-27	20,007,775.71	17,401,575.41	100%	86.97%
	Short Lead Time Items	743	05-Feb-25	05-Oct-26	11-Feb-25 A	22-Jul-27	18,899,999.75	17,018,932.25	100%	90.05%
	Infrastructure Networks	743	05-Feb-25	05-Oct-26	11-Feb-25 A	22-Jul-27	17,093,229.15	15,240,238.53	100%	89.16%
	Road Works	738	11-Feb-25	05-Oct-26	11-Feb-25 A	22-Jul-27	4,749,284.60	3,417,253.08	100%	71.95%
	Sewage Network	659	05-Feb-25	29-Mar-26	11-Feb-25 A	10-Apr-27	2,490,411.40	2,490,411.40	100%	100%
	Storm Drainage Network	586	11-Feb-25	29-Mar-26	11-Feb-25 A	16-Jan-27	4,387,027.40	4,387,027.40	100%	100%
	Potable Water Network	688	09-Feb-25	09-Feb-26	11-Feb-25 A	23-May-27	2,044,188.40	1,749,461.12	100%	85.58%
	Irrigation Network	518	11-Feb-25	21-Dec-25	11-Feb-25 A	28-Oct-26	1,248,317.60	1,223,845.80	100%	98.04%
	Medium Voltage Network	732	11-Feb-25	04-Mar-26	11-Feb-25 A	15-Jul-27	885,929.15	839,323.37	100%	94.74%
	Street Lighting Network	726	11-Feb-25	23-Jun-26	11-Feb-25 A	08-Jul-27	924,756.40	769,602.16	100%	83.22%
	Telecom Network	561	11-Feb-25	14-Jan-26	11-Feb-25 A	16-Aug-26 A	363,314.20	363,314.20	100%	100%
	Superstructure Works	617	18-Feb-25	14-Feb-26	18-Feb-25 A	17-Mar-27	1,806,770.60	1,778,693.72	100%	98.45%
	Issuance of Purchase Orders	24	18-Feb-25	18-Mar-25	18-Feb-25 A	30-Mar-25 A	0.00	0.00	0%	0%
	Manufacturing of Material	520	05-Mar-25	25-Oct-25	07-Mar-25 A	21-Nov-26	0.00	0.00	0%	0%
	1st Material Delivery & Site Inspection	346	13-Aug-25	24-Nov-25	04-Oct-25 A	21-Dec-26	0.00	0.00	0%	0%
	Material Delivery & Site Inspection	379	15-Sep-25	14-Feb-26	29-Oct-25 A	17-Mar-27	1,806,770.60	1,778,693.72	100%	98.45%
	Long Lead Time Items	662	10-Feb-25	31-Aug-26	11-Feb-25 A	08-May-27	1,107,775.96	382,643.16	100%	34.54%
	Infrastructure Networks	653	10-Feb-25	05-Feb-26	11-Feb-25 A	20-Sep-26 A	71,871.96	71,871.96	100%	100%
	RMU Works of Medium Voltage Network	653	10-Feb-25	05-Feb-26	11-Feb-25 A	20-Sep-26 A	71,871.96	71,871.96	100%	100%
	Superstructure Works	358	18-Sep-25	31-Aug-26	01-Jun-25 A	08-May-27	1,035,904.00	310,771.20	100%	30%
	Sewage Pump Stations (PS 06)	358	18-Sep-25	31-Aug-26	01-Jun-25 A	08-May-27	1,035,904.00	310,771.20	100%	30%
	Construction Works	820	09-Feb-25	28-Dec-26	11-Feb-25 A	25-Oct-27	82,973,344.90	59,246,954.51	88.58%	71.4%
	Infrastructure Networks	820	09-Feb-25	28-Dec-26	11-Feb-25 A	25-Oct-27	76,594,730.02	57,563,894.41	88.45%	75.15%
	Phase 2 Block "J"	769	09-Feb-25	01-Dec-26	11-Feb-25 A	06-Sep-27	63,588,437.54	52,494,623.96	97.67%	82.55%
	Rising Main Network	247	01-Sep-25	13-Nov-25	27-Dec-25 A	14-Dec-26	3,537,626.13	2,650,406.33	100%	74.92%
	Road 09 Local 2 (2278 LM)	621	16-Jun-25	01-Oct-26	26-Mar-25 A	07-Aug-27	21,436,707.06	16,815,930.19	100%	78.44%
	Road 10 Local 2 (2352 LM)	600	19-May-25	01-Oct-26	15-Mar-25 A	21-Jun-27	16,016,073.83	11,725,189.75	100%	73.21%
	Road 11 Local 1 (670 LM)	577	04-Aug-25	13-Oct-26	23-Apr-25 A	31-Jul-27	5,429,772.40	5,129,609.70	98.62%	94.47%
	Road 14 Local 1 (584 LM)	613	09-Jul-25	27-Oct-26	17-Apr-25 A	14-Aug-27	6,260,663.30	5,566,246.33	97.05%	88.91%
	Road 15 Local 1 (556 LM)	687	26-Apr-25	08-Nov-26	13-Apr-25 A	28-Aug-27	3,105,314.67	2,999,148.47	90.54%	96.58%
	Road 16 Local 1 (527 LM)	717	29-Mar-25	19-Nov-26	13-Mar-25 A	06-Sep-27	2,501,958.03	2,461,587.06	83.5%	98.39%
	Road 17 Local 1 (500 LM)	749	05-Mar-25	01-Dec-26	27-Feb-25 A	26-Nov-26	2,639,650.51	2,537,492.86	80.51%	96.13%
	Road 18 Local 1 (479 LM)	536	09-Feb-25	01-Jan-26	11-Feb-25 A	02-Nov-26	2,660,671.61	2,609,013.28	100%	98.06%
	Finishes for Infrastructure Networks	362	04-May-26	28-Dec-26	20-Sep-25 A	25-Oct-27	13,006,292.48	5,069,270.45	43.37%	38.98%
	Phase 2 Block "J"	362	04-May-26	28-Dec-26	20-Sep-25 A	25-Oct-27	13,006,292.48	5,069,270.45	43.37%	38.98%
	Independent Works	528	21-Jan-26	28-Dec-26	19-May-25 A	25-Oct-27	6,378,614.88	1,683,060.10	90.21%	26.39%
	Tie In To Existing Networks	148	02-Sep-26	28-Dec-26	29-Apr-27	25-Oct-27	0.00	0.00	0%	0%
	Phase 2 Block "J"	148	02-Sep-26	28-Dec-26	29-Apr-27	25-Oct-27	0.00	0.00	0%	0%
	Sewage Pump Stations	226	15-Mar-26	01-Dec-26	01-Sep-26 A	25-Jul-27	4,389,808.32	9,567.60	85.78%	0.22%
	Sewage Pump Station (PS 06)	226	15-Mar-26	01-Dec-26	01-Sep-26 A	25-Jul-27	4,389,808.32	9,567.60	85.78%	0.22%
	Storm Drainage Ponds	459	21-Jan-26	24-Aug-26	19-May-25 A	04-Aug-27	1,988,806.56	1,673,492.50	100%	84.15%
	Storm Drainage Pond (PO-J1)	344	21-Jan-26	30-Jul-26	19-May-25 A	17-Mar-27	1,702,195.30	1,673,492.50	100%	98.31%
	Storm Drainage Pond (PO-J2)	185	15-Feb-26	24-Aug-26	22-Dec-26	04-Aug-27	286,611.26	0.00	100%	0%

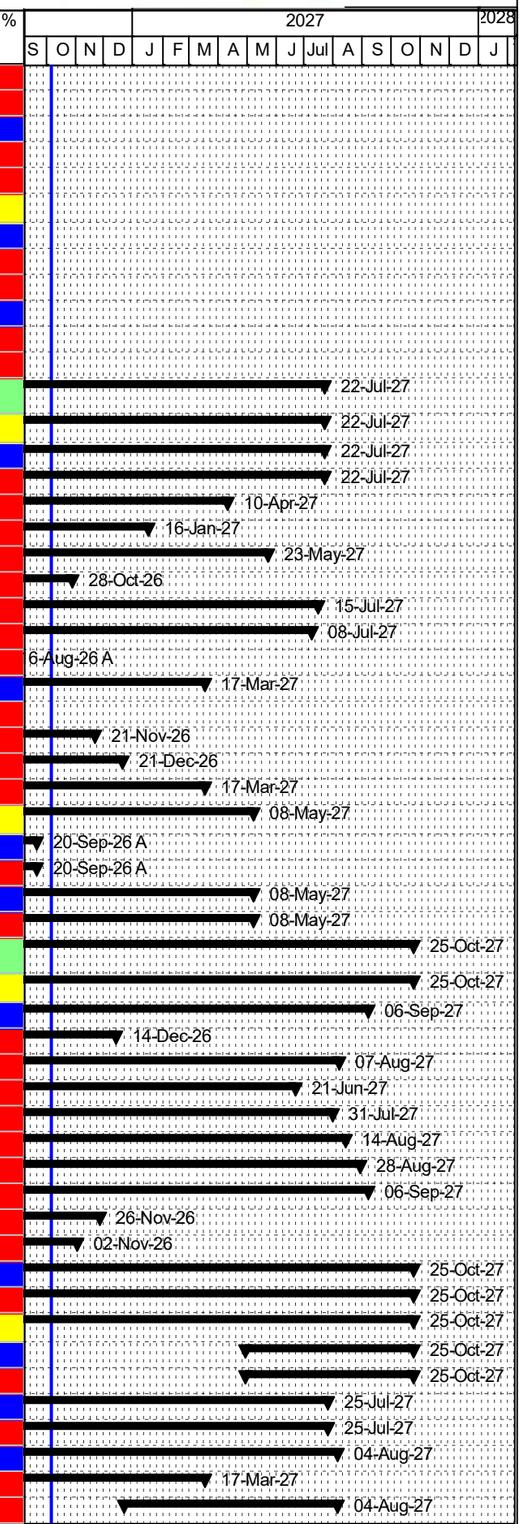


Primary Baseline | Actual Work | Summary
Remaining Work | Baseline Milestone
Critical Remaining Work | Milestone

Date	Revision	Checked	Approved
06-Oct-26	Third Industrial City		

Infrastructure Works of Area J -3rd Industrial City-
Dammam-Phase 2 - Part 2 Update 06/10/2026
WPR UPS LEVEL 5


Activity ID	Activity Name	Original Duration	BL Project Start	BL Project Finish	Start	Finish	BL Project Total Cost	Earned Value Cost	Schedule % Complete	Performance % Complete
Testing and Comissioning		130	25-Aug-26	03-Jan-27	01-Jun-26 A	31-Oct-27	11,395,586.42	7,026,149.26	2.6%	61.66%
Infrastructure Networks		118	07-Nov-26	03-Jan-27	01-Jun-26 A	31-Oct-27	11,075,668.52	7,026,149.26	0%	63.44%
Irrigation Network		12	12-Nov-26	25-Nov-26	05-Jun-26 A	10-Aug-27	624,273.76	156,068.44	0%	25%
T/C-IR	Testing and Commissioning of Irrigation Network	12	12-Nov-26	25-Nov-26	05-Jun-26 A	10-Aug-27	624,273.76	156,068.44	0%	25%
Potable Water Network		12	03-Dec-26	16-Dec-26	01-Jul-26 A	28-Sep-27	1,022,094.20	562,151.81	0%	55%
T/C-PW	Testing and Commissioning of Potable Water Network	12	03-Dec-26	16-Dec-26	01-Jul-26 A	28-Sep-27	1,022,094.20	562,151.81	0%	55%
Sewage Network		12	19-Dec-26	31-Dec-26	01-Jun-26 A	10-Oct-27	2,308,897.10	1,847,117.68	0%	80%
T/C-SW	Testing and Commissioning of Sewage Network	12	19-Dec-26	31-Dec-26	01-Jun-26 A	10-Oct-27	2,308,897.10	1,847,117.68	0%	80%
Storm Drainage Network		10	21-Dec-26	31-Dec-26	10-Jun-26 A	12-Sep-27	2,866,651.20	2,293,320.96	0%	80%
T/C-SD	Testing and Commissioning of Storm Drainage Network	10	21-Dec-26	31-Dec-26	10-Jun-26 A	12-Sep-27	2,866,651.20	2,293,320.96	0%	80%
Street Lighting Network		18	07-Nov-26	26-Nov-26	05-Sep-26 A	24-Oct-27	462,378.20	147,961.02	0%	32%
T/C-SL	Testing and Commissioning of Street Lighting Network	18	07-Nov-26	26-Nov-26	05-Sep-26 A	24-Oct-27	462,378.20	147,961.02	0%	32%
Telecom Network		10	10-Nov-26	21-Nov-26	05-Sep-26 A	20-Sep-27	181,657.10	58,130.27	0%	32%
T/C-TE	Testing and Commissioning of Telecom Network	10	10-Nov-26	21-Nov-26	05-Sep-26 A	20-Sep-27	181,657.10	58,130.27	0%	32%
Medium Voltage Network		10	22-Nov-26	02-Dec-26	05-Sep-26 A	03-Oct-27	478,905.06	239,452.53	0%	50%
T/C-MV	Testing and Commissioning of Medium Voltage Network	10	22-Nov-26	02-Dec-26	05-Sep-26 A	03-Oct-27	478,905.06	239,452.53	0%	50%
Road Works		5	29-Dec-26	03-Jan-27	16-Aug-26 A	31-Oct-27	3,130,811.90	1,721,946.55	0%	55%
T/C-RD	Testing and Commissioning of Road Works	5	29-Dec-26	03-Jan-27	16-Aug-26 A	31-Oct-27	3,130,811.90	1,721,946.55	0%	55%
Independent Works		56	25-Aug-26	31-Dec-26	05-Aug-27	10-Oct-27	319,917.90	0.00	92.79%	0%
T/C-SPS	Testing and Commissioning of Sewage Pump Stations	26	02-Dec-26	31-Dec-26	09-Sep-27	10-Oct-27	23,081.10	0.00	0%	0%
T/C-DPO	Testing and Commissioning of Storm Drainage Ponds	30	25-Aug-26	29-Sep-26	05-Aug-27	08-Sep-27	296,836.80	0.00	100%	0%
Handing over and close out		100	17-Oct-26	11-Jan-27	14-Jul-27	08-Nov-27	0.00	0.00	0%	0%
As-Built		95	17-Oct-26	05-Jan-27	14-Jul-27	02-Nov-27	0.00	0.00	0%	0%
HO-190	As-Built Drawing For Potable Water Network	12	19-Nov-26	02-Dec-26	31-Aug-27	13-Sep-27	0.00	0.00	0%	0%
HO-180	Submission As-Built Drawing For Irrigation Network	12	29-Oct-26	11-Nov-26	14-Jul-27	27-Jul-27	0.00	0.00	0%	0%
HO-170	Submission As-Built Drawing For Medium Voltage Network	12	12-Nov-26	25-Nov-26	22-Aug-27	04-Sep-27	0.00	0.00	0%	0%
HO-130	Submission As-Built Drawing For Pond	12	12-Nov-26	25-Nov-26	05-Aug-27	18-Aug-27	0.00	0.00	0%	0%
HO-210	Submission As-Built Drawing For Pump station	12	02-Dec-26	15-Dec-26	26-Jul-27	08-Aug-27	0.00	0.00	0%	0%
HO-140	Submission As-Built Drawing For Roads Network	5	29-Dec-26	03-Jan-27	25-Oct-27	31-Oct-27	0.00	0.00	0%	0%
HO-100	Submission As-Built Drawing For Sewage Network	7	29-Dec-26	05-Jan-27	25-Oct-27	02-Nov-27	0.00	0.00	0%	0%
HO-200	Submission As-Built Drawing For Storm Network	12	13-Dec-26	26-Dec-26	24-Aug-27	06-Sep-27	0.00	0.00	0%	0%
HO-150	Submission As-Built Drawing For Street Lighting Network	12	17-Oct-26	29-Oct-26	12-Sep-27	26-Sep-27	0.00	0.00	0%	0%
HO-160	Submission As-Built Drawing For Telecom Network	12	12-Nov-26	25-Nov-26	28-Jul-27	10-Aug-27	0.00	0.00	0%	0%
De-Mobilization Works		5	04-Jan-27	09-Jan-27	31-Oct-27	06-Nov-27	0.00	0.00	0%	0%
HO-120	Remove material stock & Storage area	5	04-Jan-27	09-Jan-27	31-Oct-27	06-Nov-27	0.00	0.00	0%	0%
HO-230	Remove Temporary Car Shades	5	04-Jan-27	09-Jan-27	31-Oct-27	06-Nov-27	0.00	0.00	0%	0%
HO-220	Removing Portable Caravan	5	04-Jan-27	09-Jan-27	31-Oct-27	06-Nov-27	0.00	0.00	0%	0%
Handing Over		7	04-Jan-27	11-Jan-27	31-Oct-27	08-Nov-27	0.00	0.00	0%	0%
HO-110	Final Testing Work	5	04-Jan-27	09-Jan-27	31-Oct-27	06-Nov-27	0.00	0.00	0%	0%
HO-240	Final Walkthrough and Inspection	2	10-Jan-27	11-Jan-27	06-Nov-27	08-Nov-27	0.00	0.00	0%	0%

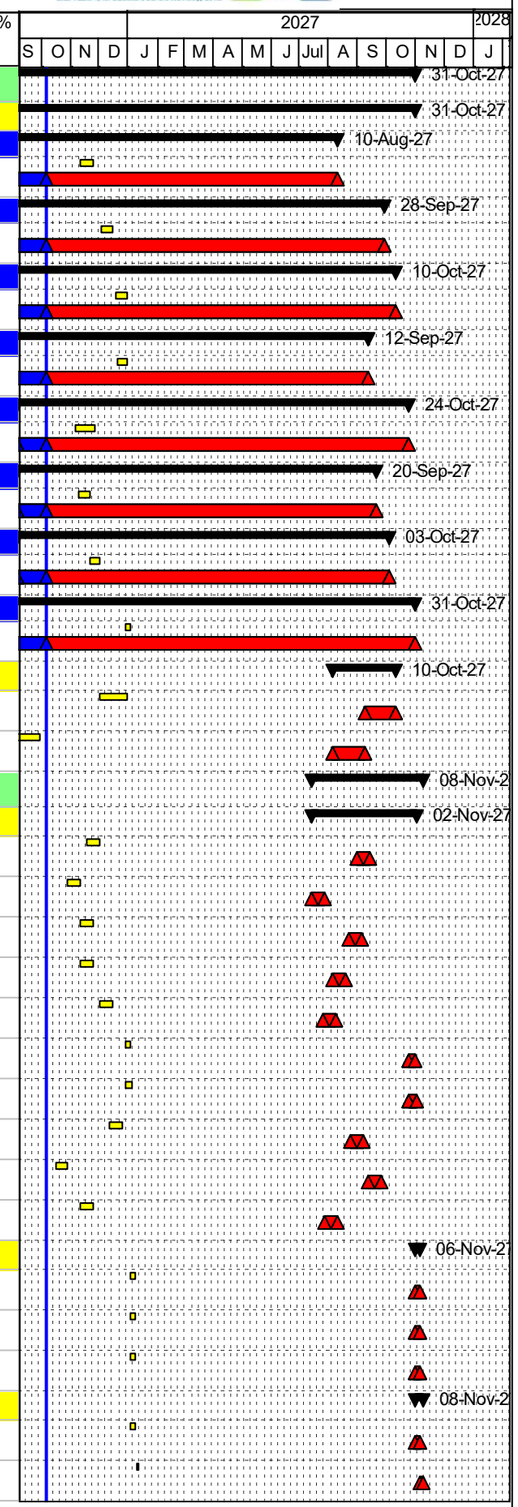

Primary Baseline · Remaining Work · Critical Remaining Work · Actual Work · Baseline Milestone · Milestone · Summary

Date	Revision	Checked	Approved
06-Oct-26	Third Industrial City		

Activity ID	Activity Name	Original Duration	BL Project Start	BL Project Finish	Start	Finish	BL Project Total Cost	Earned Value Cost	Schedule % Complete	Performance % Complete
HO-280	Punch List Completion	2	10-Jan-27	11-Jan-27	06-Nov-27	08-Nov-27	0.00	0.00	0%	0%
HO-250	Review B.O.Q Qty. to ensure compliance with the actual status	5	04-Jan-27	09-Jan-27	31-Oct-27	06-Nov-27	0.00	0.00	0%	0%
HO-260	Review FIR Approval to ensure compliance with the actual status	5	04-Jan-27	09-Jan-27	31-Oct-27	06-Nov-27	0.00	0.00	0%	0%
HO-270	Review the sample drawing to ensure compliance with the actual status	5	04-Jan-27	09-Jan-27	31-Oct-27	06-Nov-27	0.00	0.00	0%	0%



Primary Baseline
Remaining Work
Critical Remaining Work
Actual Work
Baseline Milestone
Milestone
Summary

Date	Revision	Checked	Approved
06-Oct-26	Third Industrial City		
