
Infrastructure Works of Area J -3rd Industrial City-Dammam-Phase 2 - Part 2 Update 06/10/2026

3Week Lookahead Schedule

Activity ID	Activity Name	Original Duration	Start	Finish	BL Project Start	BL Project Finish	Budgeted Total Cost
Infrastructure Works of Area J -3rd Industrial City-Dammam-Phase 2 - Part		569	01-Jun-25 A	31-Oct-27	19-Mar-25	03-Jan-27	24,088,319.58
Key Milestones		0	06-Oct-26	06-Oct-26	14-Feb-26	14-Feb-26	0.00
Control Milestones		0	06-Oct-26	06-Oct-26	14-Feb-26	14-Feb-26	0.00
MS-CS-MV	The Employer Approval NOC for Medium Voltage Network	0	06-Oct-26		14-Feb-26		0.00
Procurement Cycle		417	01-Jun-25 A	08-May-27	03-May-25	31-Aug-26	3,017,775.85
Short Lead Time Items		393	29-Oct-25 A	03-Apr-27	03-May-25	30-Apr-26	1,981,871.85
Infrastructure Networks		383	13-Dec-25 A	03-Apr-27	03-May-25	30-Apr-26	1,388,198.25
Road Works		32	06-Oct-26	11-Nov-26	20-Jul-25	30-Apr-26	618,180.02
1st Material Delivery & Site Inspection		6	06-Oct-26	12-Oct-26	20-Jul-25	18-Aug-25	0.00
Pavement Works		6	06-Oct-26	12-Oct-26	20-Jul-25	26-Jul-25	0.00
PRO-RD-1DL-140	1ST Material Delivery for Interlock Tiles of Landscaping	6	06-Oct-26	12-Oct-26	20-Jul-25	26-Jul-25	0.00
PRO-RD-1DL-150	1ST Material Delivery for Curbstones of Landscaping	6	06-Oct-26	12-Oct-26	20-Jul-25	26-Jul-25	0.00
Traffic Signs Boards and Roads Marking		6	06-Oct-26	12-Oct-26	12-Aug-25	18-Aug-25	0.00
PRO-RD-1DL-160	1ST Material Delivery for Traffic Signs Boards of Road Works	6	06-Oct-26	12-Oct-26	12-Aug-25	18-Aug-25	0.00
PRO-RD-1DL-170	1ST Material Delivery for Road Markings of Road Works	6	06-Oct-26	12-Oct-26	12-Aug-25	18-Aug-25	0.00
Material Delivery & Site Inspection		26	13-Oct-26	11-Nov-26	28-Dec-25	30-Apr-26	618,180.02
Road 18 Local 1 (479 LM)		26	13-Oct-26	11-Nov-26	28-Dec-25	26-Jan-26	1,971.20
Traffic Signs Boards and Roads Marking		26	13-Oct-26	11-Nov-26	28-Dec-25	26-Jan-26	1,971.20
PRO-R18-RD-DL	Material Delivery & Site Inspection of Traffic Signs Boards For Road Works	26	13-Oct-26	11-Nov-26	28-Dec-25	26-Jan-26	1,971.20
Road 10 Local 2 (2352 LM)		26	13-Oct-26	11-Nov-26	26-Feb-26	30-Apr-26	616,208.82
Bituminous Construction		26	13-Oct-26	11-Nov-26	26-Feb-26	30-Apr-26	616,208.82
PRO-R10-RD-DL	Material Delivery & Site Inspection for Prime Coat of Road Works	26	13-Oct-26	11-Nov-26	26-Feb-26	31-Mar-26	123,242.68
PRO-R10-RD-DL	Material Delivery & Site Inspection for Bituminous Base & Wearing Courses of Road	26	13-Oct-26	11-Nov-26	01-Apr-26	30-Apr-26	492,966.14
Sewage Network		38	06-Oct-26	18-Nov-26	26-Jul-25	25-Oct-25	0.00
Material Delivery & Site Inspection		38	06-Oct-26	18-Nov-26	26-Jul-25	25-Oct-25	0.00
Road 17 Local 1 (500 LM)		26	06-Oct-26	04-Nov-26	25-Aug-25	25-Oct-25	0.00
Testing and Finishes		26	06-Oct-26	04-Nov-26	25-Aug-25	25-Oct-25	0.00
PRO-R17-SW-DL	Material Delivery & Site Inspection of Manholes Covers for Sewage Network	26	06-Oct-26	04-Nov-26	25-Aug-25	24-Sep-25	0.00
PRO-R17-SW-DL	Material Delivery & Site Inspection of Membrane Insulation for Sewage Network	26	06-Oct-26	04-Nov-26	25-Sep-25	25-Oct-25	0.00
Road 09 Local 2 (2278 LM)		38	06-Oct-26	18-Nov-26	26-Jul-25	07-Sep-25	0.00
Testing and Finishes		38	06-Oct-26	18-Nov-26	26-Jul-25	07-Sep-25	0.00
PRO-R09-SW-DL	Material Delivery & Site Inspection of Manholes Covers for Rising Main Network	38	06-Oct-26	18-Nov-26	26-Jul-25	07-Sep-25	0.00
PRO-R09-SW-DL	Material Delivery & Site Inspection of Membrane Insulation for Rising Main Network	38	06-Oct-26	18-Nov-26	26-Jul-25	07-Sep-25	0.00
Storm Drainage Network		113	20-Jun-26 A	16-Nov-26	26-Jul-25	24-Jan-26	0.00
Material Delivery & Site Inspection		113	20-Jun-26 A	16-Nov-26	26-Jul-25	24-Jan-26	0.00
Road 18 Local 1 (479 LM)		26	27-Jun-26 A	17-Oct-26	26-Jul-25	24-Aug-25	0.00
Testing and Finishes		26	27-Jun-26 A	17-Oct-26	26-Jul-25	24-Aug-25	0.00
PRO-R18-SD-DL·	Material Delivery & Site Inspection of Manholes Covers for Storm Drainage Network	26	27-Jun-26 A	17-Oct-26	26-Jul-25	24-Aug-25	0.00
PRO-R18-SD-DL·	Material Delivery & Site Inspection of Catch Basin Covers for Storm Drainage Netwo	26	27-Jun-26 A	17-Oct-26	26-Jul-25	24-Aug-25	0.00
PRO-R18-SD-DL·	Material Delivery & Site Inspection of Epoxy Insulation for Storm Drainage Network	26	27-Jun-26 A	17-Oct-26	26-Jul-25	24-Aug-25	0.00
Road 17 Local 1 (500 LM)		26	20-Jun-26 A	28-Oct-26	25-Aug-25	24-Sep-25	0.00
Testing and Finishes		26	20-Jun-26 A	28-Oct-26	25-Aug-25	24-Sep-25	0.00
PRO-R17-SD-DL·	Material Delivery & Site Inspection of Manholes Covers for Storm Drainage Network	26	20-Jun-26 A	28-Oct-26	25-Aug-25	24-Sep-25	0.00
PRO-R17-SD-DL·	Material Delivery & Site Inspection of Catch Basin Covers for Storm Drainage Netwo	26	20-Jun-26 A	28-Oct-26	25-Aug-25	24-Sep-25	0.00
PRO-R17-SD-DL·	Material Delivery & Site Inspection of Epoxy Insulation for Storm Drainage Network	26	20-Jun-26 A	28-Oct-26	25-Aug-25	24-Sep-25	0.00
Road 16 Local 1 (527 LM)		26	18-Oct-26	16-Nov-26	25-Sep-25	25-Oct-25	0.00
Testing and Finishes		26	18-Oct-26	16-Nov-26	25-Sep-25	25-Oct-25	0.00
PRO-R16-SD-DL·	Material Delivery & Site Inspection of Manholes Covers for Storm Drainage Network	26	18-Oct-26	16-Nov-26	25-Sep-25	25-Oct-25	0.00
PRO-R16-SD-DL·	Material Delivery & Site Inspection of Catch Basin Covers for Storm Drainage Netwo	26	18-Oct-26	16-Nov-26	25-Sep-25	25-Oct-25	0.00
PRO-R16-SD-DL·	Material Delivery & Site Inspection of Epoxy Insulation for Storm Drainage Network	26	18-Oct-26	16-Nov-26	25-Sep-25	25-Oct-25	0.00
Road 15 Local 1 (556 LM)		26	18-Oct-26	16-Nov-26	26-Oct-25	24-Nov-25	0.00
Testing and Finishes		26	18-Oct-26	16-Nov-26	26-Oct-25	24-Nov-25	0.00

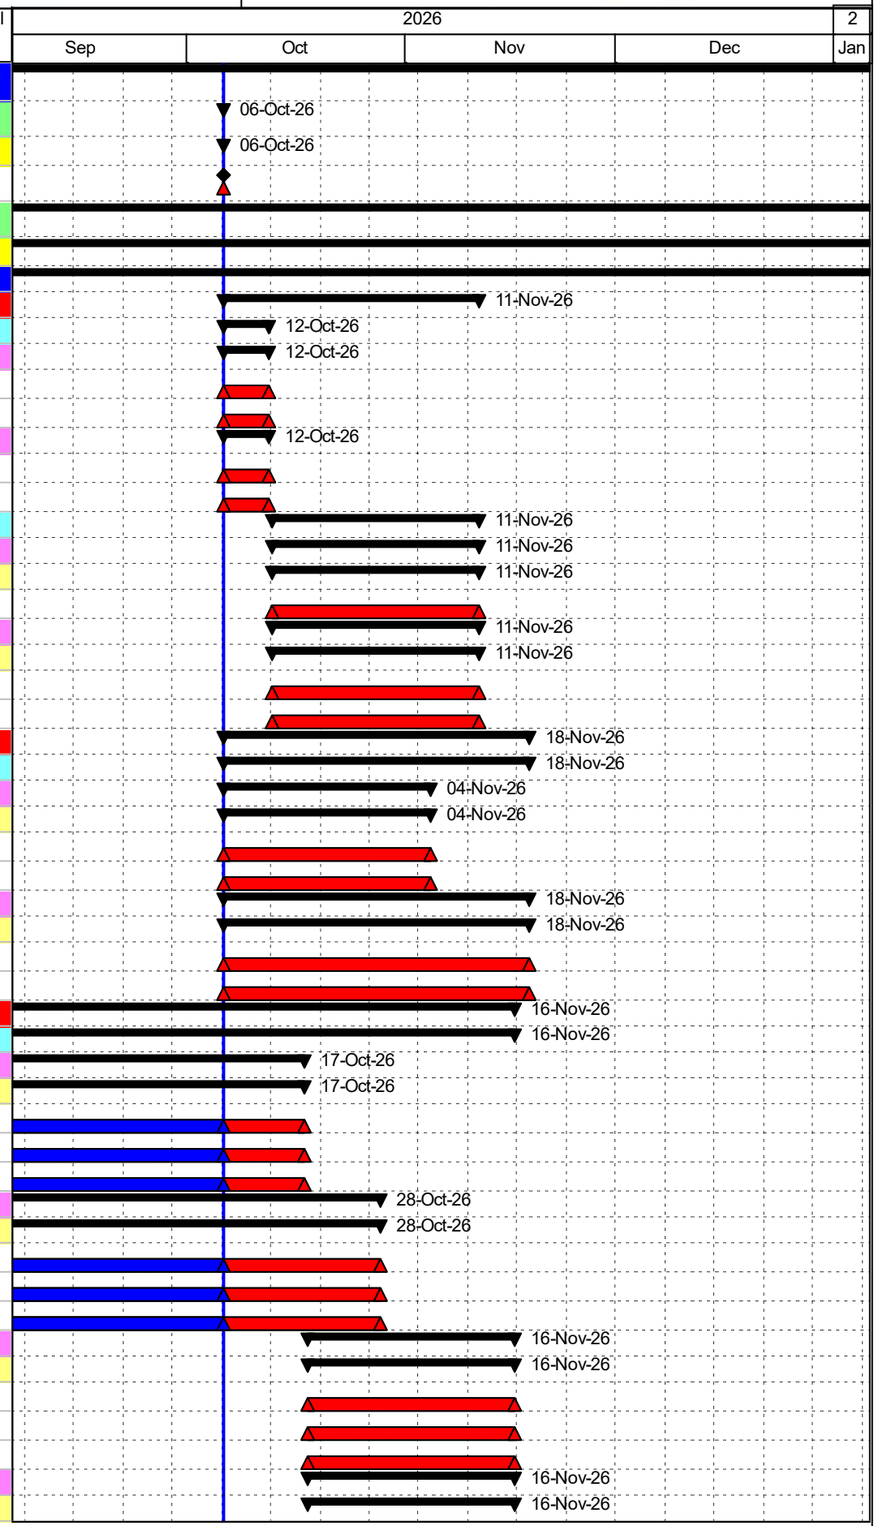


Primary Baseline · Remaining Work · Critical Remaining Work · Actual Work · Baseline Milestone · Milestone · Summary

Date	Revision	Checked	Approved
06-Oct-26	Third Industrial City		

Infrastructure Works of Area J -3rd Industrial City-
Dammam-Phase 2 - Part 2 Update 06/10/2026
3Week Lookahead Schedule

Activity ID	Activity Name	Original Duration	Start	Finish	BL Project Start	BL Project Finish	Budgeted Total Cost
PRO-R15-SD-DL·	Material Delivery & Site Inspection of Manholes Covers for Storm Drainage Network	26	18-Oct-26	16-Nov-26	26-Oct-25	24-Nov-25	0.00
PRO-R15-SD-DL·	Material Delivery & Site Inspection of Catch Basin Covers for Storm Drainage Netwo	26	18-Oct-26	16-Nov-26	26-Oct-25	24-Nov-25	0.00
PRO-R15-SD-DL·	Material Delivery & Site Inspection of Epoxy Insulation for Storm Drainage Network	26	18-Oct-26	16-Nov-26	26-Oct-25	24-Nov-25	0.00
Road 10 Local 2 (2352 LM)		26	18-Oct-26	16-Nov-26	25-Nov-25	24-Dec-25	0.00
Testing and Finishes		26	18-Oct-26	16-Nov-26	25-Nov-25	24-Dec-25	0.00
PRO-R10-SD-DL·	Material Delivery & Site Inspection of Manholes Covers for Storm Drainage Network	26	18-Oct-26	16-Nov-26	25-Nov-25	24-Dec-25	0.00
PRO-R10-SD-DL·	Material Delivery & Site Inspection of Catch Basin Covers for Storm Drainage Netwo	26	18-Oct-26	16-Nov-26	25-Nov-25	24-Dec-25	0.00
PRO-R10-SD-DL·	Material Delivery & Site Inspection of Epoxy Insulation for Storm Drainage Network	26	18-Oct-26	16-Nov-26	25-Nov-25	24-Dec-25	0.00
Road 14 Local 1 (584 LM)		26	18-Oct-26	16-Nov-26	25-Dec-25	24-Jan-26	0.00
Testing and Finishes		26	18-Oct-26	16-Nov-26	25-Dec-25	24-Jan-26	0.00
PRO-R14-SD-DL·	Material Delivery & Site Inspection of Manholes Covers for Storm Drainage Network	26	18-Oct-26	16-Nov-26	25-Dec-25	24-Jan-26	0.00
PRO-R14-SD-DL·	Material Delivery & Site Inspection of Catch Basin Covers for Storm Drainage Netwo	26	18-Oct-26	16-Nov-26	25-Dec-25	24-Jan-26	0.00
PRO-R14-SD-DL·	Material Delivery & Site Inspection of Epoxy Insulation for Storm Drainage Network	26	18-Oct-26	16-Nov-26	25-Dec-25	24-Jan-26	0.00
Potable Water Network		250	13-Dec-25 A	05-Dec-26	31-May-25	15-Oct-25	229,741.60
1st Material Delivery & Site Inspection		6	06-Oct-26	12-Oct-26	31-May-25	10-Jun-25	0.00
Testing and Finishes		6	06-Oct-26	12-Oct-26	31-May-25	10-Jun-25	0.00
PRO-PW-1DL-130	1ST Material Delivery for Finishes of Potable Water Network	6	06-Oct-26	12-Oct-26	31-May-25	10-Jun-25	0.00
Material Delivery & Site Inspection		250	13-Dec-25 A	05-Dec-26	11-Jun-25	15-Oct-25	229,741.60
Road 18 Local 1 (479 LM)		26	13-Oct-26	11-Nov-26	11-Jun-25	10-Jul-25	0.00
Testing and Finishes		26	13-Oct-26	11-Nov-26	11-Jun-25	10-Jul-25	0.00
PRO-R18-PW-DL	Material Delivery & Site Inspection for Finishes of Potable Water Network	26	13-Oct-26	11-Nov-26	11-Jun-25	10-Jul-25	0.00
Road 17 Local 1 (500 LM)		26	06-Oct-26	04-Nov-26	16-Jun-25	15-Jul-25	5,532.80
Main Line Sections		26	06-Oct-26	04-Nov-26	16-Jun-25	15-Jul-25	5,532.80
PRO-R17-PW-DL	Material Delivery & Site Inspection of Valves for Potable Water Network	26	06-Oct-26	04-Nov-26	16-Jun-25	15-Jul-25	5,532.80
Road 16 Local 1 (527 LM)		26	06-Oct-26	04-Nov-26	16-Jul-25	14-Aug-25	3,952.00
Main Line Sections		26	06-Oct-26	04-Nov-26	16-Jul-25	14-Aug-25	3,952.00
PRO-R16-PW-DL	Material Delivery & Site Inspection of Valves for Potable Water Network	26	06-Oct-26	04-Nov-26	16-Jul-25	14-Aug-25	3,952.00
Road 15 Local 1 (556 LM)		26	06-Oct-26	04-Nov-26	16-Aug-25	14-Sep-25	4,742.40
Main Line Sections		26	06-Oct-26	04-Nov-26	16-Aug-25	14-Sep-25	4,742.40
PRO-R15-PW-DL	Material Delivery & Site Inspection of Valves for Potable Water Network	26	06-Oct-26	04-Nov-26	16-Aug-25	14-Sep-25	4,742.40
Road 10 Local 2 (2352 LM)		26	13-Dec-25 A	05-Dec-26	15-Sep-25	15-Oct-25	215,514.40
Main Line Sections		26	13-Dec-25 A	05-Dec-26	15-Sep-25	15-Oct-25	215,514.40
PRO-R10-PW-DL	Material Delivery & Site Inspection of Valves for Potable Water Network	26	13-Dec-25 A	05-Dec-26	15-Sep-25	15-Oct-25	215,514.40
Irrigation Network		20	06-Oct-26	28-Oct-26	17-Jul-25	07-Oct-25	24,471.80
1st Material Delivery & Site Inspection		6	06-Oct-26	12-Oct-26	17-Jul-25	23-Jul-25	0.00
Main Line Pipes		6	06-Oct-26	12-Oct-26	17-Jul-25	23-Jul-25	0.00
PRO-IR-1DL-110	1ST Material Delivery for Valves of Irrigation Network	6	06-Oct-26	12-Oct-26	17-Jul-25	23-Jul-25	0.00
Material Delivery & Site Inspection		20	06-Oct-26	28-Oct-26	24-Jul-25	07-Oct-25	24,471.80
Road 18 Local 1 (479 LM)		7	06-Oct-26	13-Oct-26	24-Jul-25	11-Aug-25	4,631.80
Main Line Pipes		7	06-Oct-26	13-Oct-26	24-Jul-25	11-Aug-25	4,631.80
PRO-R18-IR-DL-·	Material Delivery & Site Inspection of Valves for Irrigation Network	7	06-Oct-26	13-Oct-26	24-Jul-25	11-Aug-25	4,631.80
Road 17 Local 1 (500 LM)		7	14-Oct-26	21-Oct-26	12-Aug-25	30-Aug-25	10,795.40
Main Line Pipes		7	14-Oct-26	21-Oct-26	12-Aug-25	30-Aug-25	10,795.40
PRO-R17-IR-DL-·	Material Delivery & Site Inspection of Valves for Irrigation Network	7	14-Oct-26	21-Oct-26	12-Aug-25	30-Aug-25	10,795.40
Road 16 Local 1 (527 LM)		7	14-Oct-26	21-Oct-26	31-Aug-25	17-Sep-25	5,474.60
Main Line Pipes		7	14-Oct-26	21-Oct-26	31-Aug-25	17-Sep-25	5,474.60
PRO-R16-IR-DL-·	Material Delivery & Site Inspection of Valves for Irrigation Network	7	14-Oct-26	21-Oct-26	31-Aug-25	17-Sep-25	5,474.60
Road 15 Local 1 (556 LM)		6	22-Oct-26	28-Oct-26	18-Sep-25	07-Oct-25	3,570.00
Main Line Pipes		6	22-Oct-26	28-Oct-26	18-Sep-25	07-Oct-25	3,570.00
PRO-R15-IR-DL-·	Material Delivery & Site Inspection of Valves for Irrigation Network	6	22-Oct-26	28-Oct-26	18-Sep-25	07-Oct-25	3,570.00
Medium Voltage Network		296	13-Dec-25 A	05-Dec-26	03-May-25	20-Dec-25	359,337.77
1st Material Delivery & Site Inspection		52	06-Oct-26	05-Dec-26	03-May-25	10-Nov-25	0.00
RMU Concrete Works		52	06-Oct-26	05-Dec-26	10-Sep-25	10-Nov-25	0.00
PRO-MV-1DL-110	1ST Material Delivery for RMU Concrete Foundations of Medium Voltage Network	52	06-Oct-26	05-Dec-26	10-Sep-25	10-Nov-25	0.00

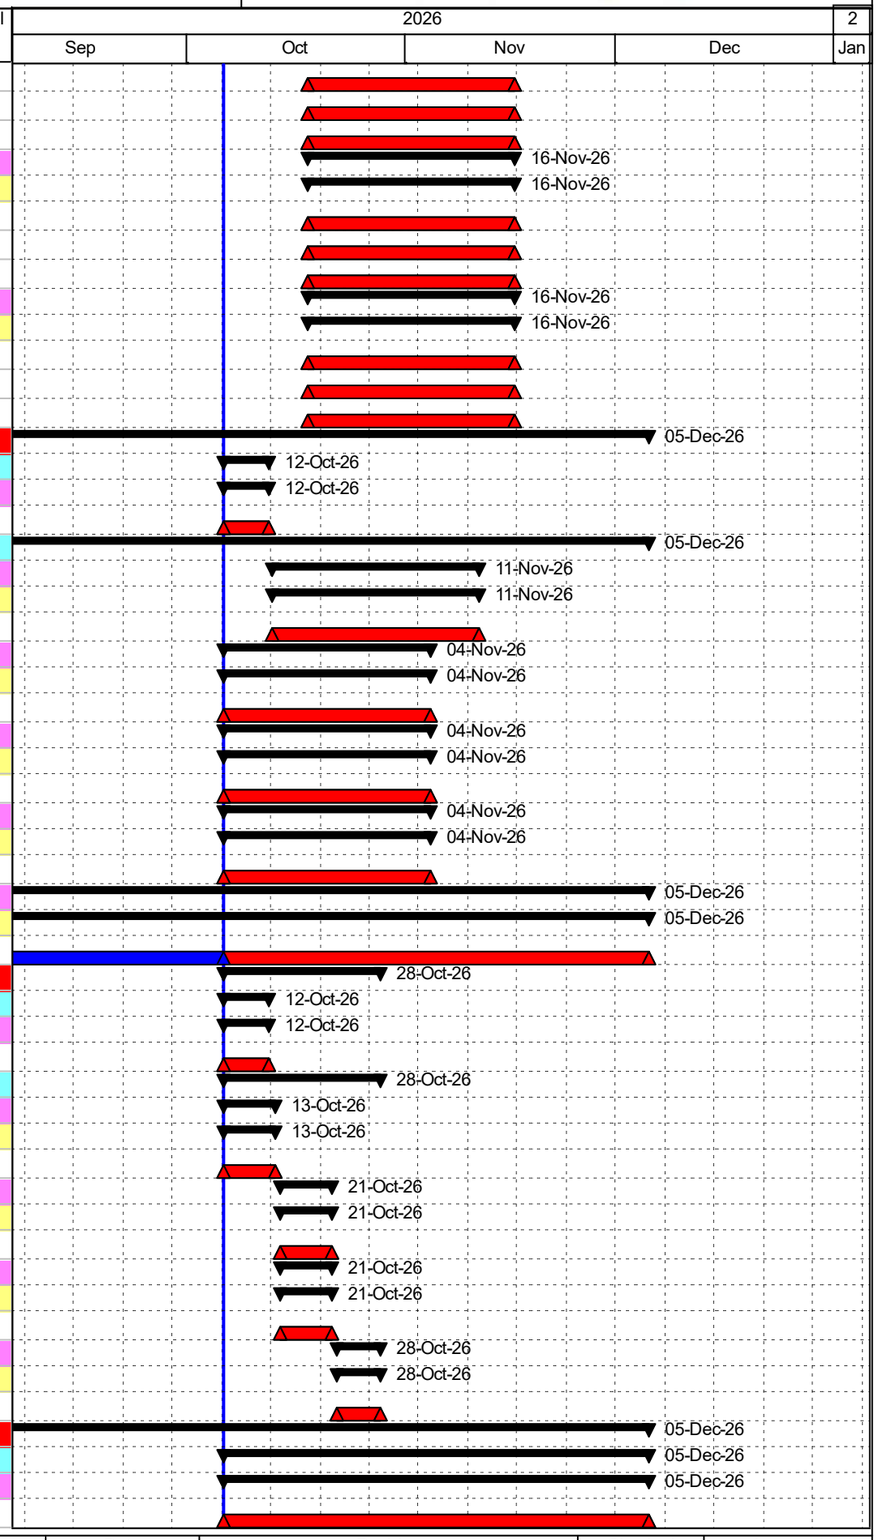


Primary Baseline
Remaining Work
Critical Remaining Work
Actual Work
Baseline Milestone
Milestone
Summary

Date	Revision	Checked	Approved
06-Oct-26	Third Industrial City		

Infrastructure Works of Area J -3rd Industrial City-
Dammam-Phase 2 - Part 2 Update 06/10/2026
3Week Lookahead Schedule


Activity ID	Activity Name	Original Duration	Start	Finish	BL Project Start	BL Project Finish	Budgeted Total Cost
Termination and Testing Works		26	06-Oct-26	04-Nov-26	03-May-25	01-Jun-25	0.00
PRO-MV-1DL-120	1ST Material Delivery for Termination and Joints Kits of Medium Voltage Network	26	06-Oct-26	04-Nov-26	03-May-25	01-Jun-25	0.00
Material Delivery & Site Inspection		26	13-Dec-25 A	04-Nov-26	20-Nov-25	20-Dec-25	359,337.77
Road 09 Local 2 (2278 LM)		26	13-Dec-25 A	04-Nov-26	20-Nov-25	20-Dec-25	359,337.77
Cabling Works		26	13-Dec-25 A	04-Nov-26	20-Nov-25	20-Dec-25	359,337.77
PRO-R09-MV-DL-	Material Delivery & Site Inspection of Medium Voltage Cables for Medium Voltage N	26	13-Dec-25 A	04-Nov-26	20-Nov-25	20-Dec-25	359,337.77
Street Lighting Network		144	21-Sep-26 A	03-Apr-27	26-Jul-25	16-Mar-26	156,467.06
1st Material Delivery & Site Inspection		15	06-Oct-26	22-Oct-26	26-Jul-25	11-Aug-25	0.00
Lighting Poles Works		6	06-Oct-26	12-Oct-26	26-Jul-25	31-Jul-25	0.00
PRO-SL-1DL-140	1ST Material Delivery for Lighting Fixtures of Street Lighting Network	6	06-Oct-26	12-Oct-26	26-Jul-25	31-Jul-25	0.00
Distribution Panel Board		6	06-Oct-26	12-Oct-26	26-Jul-25	31-Jul-25	0.00
PRO-SL-1DL-160	1ST Material Delivery for Distrubution Panel Boards of Street Lighting Network	6	06-Oct-26	12-Oct-26	26-Jul-25	31-Jul-25	0.00
Termination and Testing Works		15	06-Oct-26	22-Oct-26	26-Jul-25	11-Aug-25	0.00
PRO-SL-1DL-130	1ST Material Delivery for Fuse Boxes of Street Lighting Network	6	06-Oct-26	12-Oct-26	26-Jul-25	11-Aug-25	0.00
PRO-SL-1DL-170	1ST Material Delivery for Cable Lugs of Street Lighting Network	15	06-Oct-26	22-Oct-26	26-Jul-25	11-Aug-25	0.00
Earthing System Works		6	06-Oct-26	12-Oct-26	26-Jul-25	31-Jul-25	0.00
PRO-SL-1DL-150	1ST Material Delivery for Lighting Earthing of Street Lighting Network	6	06-Oct-26	12-Oct-26	26-Jul-25	31-Jul-25	0.00
Material Delivery & Site Inspection		144	21-Sep-26 A	03-Apr-27	02-Aug-25	16-Mar-26	156,467.06
Road 18 Local 1 (479 LM)		14	13-Oct-26	28-Oct-26	16-Aug-25	15-Oct-25	8,511.96
Lighting Poles Works		10	13-Oct-26	24-Oct-26	16-Aug-25	14-Sep-25	3,754.80
PRO-R18-SL-DL-	Material Delivery & Site Inspection of Lighting Fixtures for Street Lighting Network	10	13-Oct-26	24-Oct-26	16-Aug-25	14-Sep-25	3,754.80
Termination and Testing Works		14	13-Oct-26	28-Oct-26	15-Sep-25	15-Oct-25	4,757.16
PRO-R18-SL-DL-	Material Delivery & Site Inspection of Fuse Boxes for Street Lighting Network	14	13-Oct-26	28-Oct-26	15-Sep-25	15-Oct-25	4,757.16
Road 17 Local 1 (500 LM)		36	13-Oct-26	23-Nov-26	15-Sep-25	15-Nov-25	8,014.22
Lighting Poles Works		26	25-Oct-26	23-Nov-26	15-Sep-25	15-Oct-25	3,933.60
PRO-R17-SL-DL-	Material Delivery & Site Inspection of Lighting Fixtures for Street Lighting Network	26	25-Oct-26	23-Nov-26	15-Sep-25	15-Oct-25	3,933.60
Termination and Testing Works		26	13-Oct-26	11-Nov-26	16-Oct-25	15-Nov-25	4,080.62
PRO-R17-SL-DL-	Material Delivery & Site Inspection of Fuse Boxes for Street Lighting Network	26	13-Oct-26	11-Nov-26	16-Oct-25	15-Nov-25	4,080.62
Road 16 Local 1 (527 LM)		26	13-Oct-26	11-Nov-26	16-Nov-25	15-Dec-25	4,150.18
Termination and Testing Works		26	13-Oct-26	11-Nov-26	16-Nov-25	15-Dec-25	4,150.18
PRO-R16-SL-DL-	Material Delivery & Site Inspection of Fuse Boxes for Street Lighting Network	26	13-Oct-26	11-Nov-26	16-Nov-25	15-Dec-25	4,150.18
Road 10 Local 2 (2352 LM)		144	21-Sep-26 A	03-Apr-27	02-Aug-25	16-Mar-26	132,272.70
Distribution Panel Board		26	21-Sep-26 A	11-Nov-26	02-Aug-25	31-Aug-25	103,537.20
PRO-R10-SL-DL-	Material Delivery & Site Inspection of Distrubution Panel Boards for Street Lighting N	26	21-Sep-26 A	11-Nov-26	02-Aug-25	31-Aug-25	103,537.20
Termination and Testing Works		92	21-Sep-26 A	03-Apr-27	15-Jan-26	16-Mar-26	25,217.50
PRO-R10-SL-DL-	Material Delivery & Site Inspection of Fuse Boxes for Street Lighting Network	26	21-Sep-26 A	11-Jan-27	15-Jan-26	14-Feb-26	25,217.50
PRO-R10-SL-DL-	Material Delivery & Site Inspection of Cable Lugs for Street Lighting Network	26	21-Sep-26 A	03-Apr-27	15-Feb-26	16-Mar-26	0.00
Earthing System Works		26	13-Oct-26	11-Nov-26	02-Aug-25	31-Aug-25	3,518.00
PRO-R10-SL-DL-	Material Delivery & Site Inspection of Lighting Earthing for Street Lighting Network	26	13-Oct-26	11-Nov-26	02-Aug-25	31-Aug-25	3,518.00
Road 09 Local 2 (2278 LM)		26	13-Oct-26	11-Nov-26	02-Aug-25	31-Aug-25	3,518.00
Earthing System Works		26	13-Oct-26	11-Nov-26	02-Aug-25	31-Aug-25	3,518.00
PRO-R09-SL-DL-	Material Delivery & Site Inspection of Lighting Earthing for Street Lighting Network	26	13-Oct-26	11-Nov-26	02-Aug-25	31-Aug-25	3,518.00
Superstructure Works		379	29-Oct-25 A	17-Mar-27	13-Aug-25	14-Feb-26	593,673.60
Manufacturing of Material		40	06-Oct-26	21-Nov-26	16-Aug-25	25-Oct-25	0.00
Storm Drainage Ponds (PO-J1 , PO-J2)		40	06-Oct-26	21-Nov-26	16-Aug-25	25-Oct-25	0.00
PRO-DPO-CV-MF-2	Manufacturing of Civil Works for Storm Drainage Ponds (PO-J2)	40	06-Oct-26	21-Nov-26	16-Aug-25	25-Oct-25	0.00
1st Material Delivery & Site Inspection		40	06-Oct-26	21-Nov-26	13-Aug-25	29-Sep-25	0.00
Sewage Pump Stations (PS 06)		40	06-Oct-26	21-Nov-26	13-Aug-25	29-Sep-25	0.00
PRO-SPS-CV-1DL-	1ST Material Delivery for Civil Works for Sewage Pump Stations (PS 06)	40	06-Oct-26	21-Nov-26	13-Aug-25	29-Sep-25	0.00
Material Delivery & Site Inspection		379	29-Oct-25 A	17-Mar-27	15-Sep-25	14-Feb-26	593,673.60
Storm Drainage Ponds (PO-J1 , PO-J2)		379	29-Oct-25 A	17-Mar-27	15-Sep-25	14-Feb-26	593,673.60
PRO-DPO-CV-DL-1	Material Delivery & Site Inspection for Civil Works for Storm Drainage Ponds (PO-J1	70	29-Oct-25 A	26-Dec-26	15-Sep-25	06-Dec-25	508,118.00
PRO-DPO-CV-DL-2	Material Delivery & Site Inspection for Civil Works for Storm Drainage Ponds (PO-J2	70	09-Sep-26 A	17-Mar-27	25-Nov-25	14-Feb-26	85,555.60
Long Lead Time Items		298	01-Jun-25 A	08-May-27	29-Nov-25	31-Aug-26	1,035,904.00

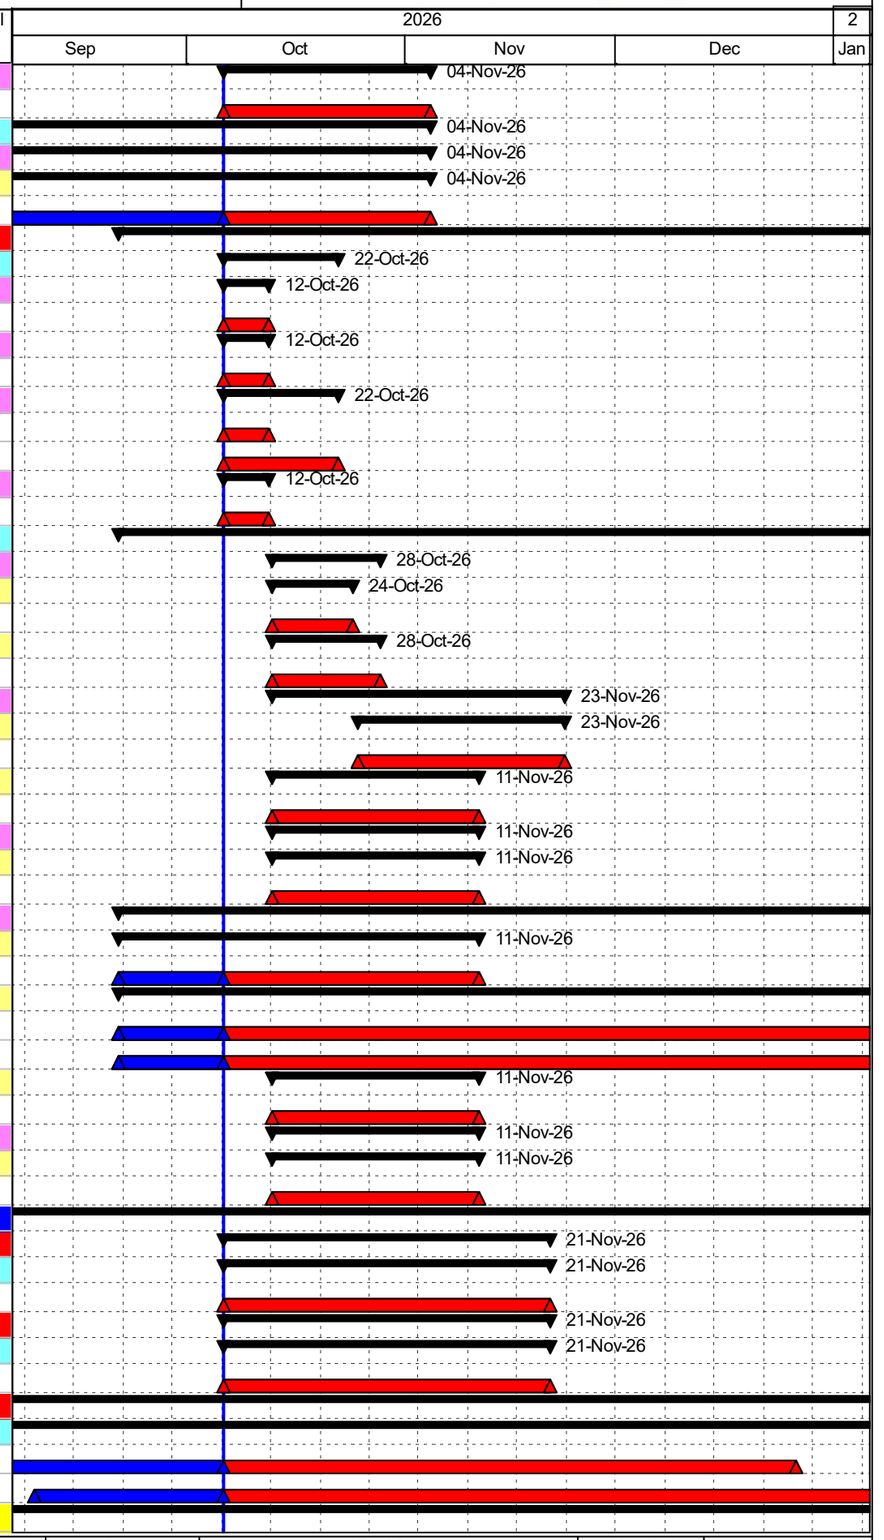

Primary Baseline · Remaining Work · Critical Remaining Work · Actual Work · Baseline Milestone · Milestone · Summary

Date	Revision	Checked	Approved
06-Oct-26	Third Industrial City		

Activity ID	Activity Name	Original Duration	Start	Finish	BL Project Start	BL Project Finish	Budgeted Total Cost
Superstructure Works		298	01-Jun-25 A	08-May-27	29-Nov-25	31-Aug-26	1,035,904.00
Sewage Pump Stations (PS 06)		298	01-Jun-25 A	08-May-27	29-Nov-25	31-Aug-26	1,035,904.00
Manufacturing of Material		100	01-Jun-25 A	02-Dec-26	29-Nov-25	28-Mar-26	0.00
PRO-SPS7-LL-MF-1	Manufacturing of Electromechanical Works for Sewage Pump Stations (PS 06)	100	01-Jun-25 A	02-Dec-26	29-Nov-25	28-Mar-26	0.00
Material Site Inspection		50	15-Sep-26 A	08-May-27	05-Jul-26	31-Aug-26	1,035,904.00
PRO-SPS7-LL-MSI-	Material Site Inspection for Electromechanical Works for Sewage Pump Stations (PS	50	15-Sep-26 A	08-May-27	05-Jul-26	31-Aug-26	1,035,904.00
Construction Works		531	10-Nov-25 A	06-Sep-27	19-Mar-25	19-Nov-26	9,994,875.22
Infrastructure Networks		531	10-Nov-25 A	06-Sep-27	19-Mar-25	19-Nov-26	9,922,161.46
Phase 2 Block "J"		531	10-Nov-25 A	06-Sep-27	19-Mar-25	19-Nov-26	8,125,205.48
Rising Main Network		240	17-Jan-26 A	14-Dec-26	27-Sep-25	13-Nov-25	2,460,387.57
Main Line Sections		226	25-Feb-26 A	14-Dec-26	27-Sep-25	13-Nov-25	1,336,085.86
CO-RM-SW-300	Pipes Laying Works for Main Lines of Rising Main Network	21	25-Feb-26 A	19-Nov-26	27-Sep-25	20-Oct-25	1,169,075.13
CO-RM-SW-310	Trench Backfilling and Compaction Works for Main Lines of Rising Main Network	21	01-Sep-26 A	14-Dec-26	21-Oct-25	13-Nov-25	167,010.73
Manholes		215	17-Jan-26 A	15-Nov-26	28-Sep-25	16-Oct-25	734,847.22
CO-RM-SW-330	Installation RC Footing Works for Main Line Manholes of Rising Main Network	3	17-Jan-26 A	29-Oct-26	28-Sep-25	30-Sep-25	66,804.29
CO-RM-SW-340	Install Grp Liner Wall Works for Main Line Manholes of Rising Main Network	6	17-Jan-26 A	05-Nov-26	01-Oct-25	07-Oct-25	501,032.20
CO-RM-SW-350	Pouring Grp Liner Wall Works for Main Line Manholes of Rising Main Network	3	18-Sep-26 A	09-Nov-26	08-Oct-25	11-Oct-25	66,804.29
CO-RM-SW-360	Backfilling Works for Main Line Manholes of Rising Main Network	5	21-Sep-26 A	15-Nov-26	12-Oct-25	16-Oct-25	100,206.44
Valves Chamber		7	14-May-26 A	27-Oct-26	05-Oct-25	12-Oct-25	389,454.48
CO-RM-SW-400	RC Wall Works for Valve Chambers and Washout chamber of Rising Main Network	7	14-May-26 A	27-Oct-26	05-Oct-25	12-Oct-25	389,454.48
Road 09 Local 2 (2278 LM)		494	10-Nov-25 A	07-Aug-27	21-Jul-25	01-Oct-26	2,351,018.40
SW_1		293	02-May-26 A	31-Jul-27	11-Aug-25	24-Sep-26	1,319,316.10
Sewage Network		1	06-Oct-26	06-Oct-26	11-Aug-25	11-Aug-25	35,494.42
Manholes		1	06-Oct-26	06-Oct-26	11-Aug-25	11-Aug-25	35,494.42
CO-R09.S01-SW-	Testing Works for Main Line Manholes of Sewage Network-[Road 09] -[SW-1]	1	06-Oct-26	06-Oct-26	11-Aug-25	11-Aug-25	35,494.42
Storm Drainage Network		97	27-Jun-26 A	12-Nov-26	05-Oct-25	18-Nov-25	287,863.46
Manholes		2	07-Oct-26	08-Oct-26	05-Oct-25	06-Oct-25	38,388.86
CO-R09.S01-SD-	Testing Works for Manholes of Storm Drainage Network-[Road 09] -[SW-1]	2	07-Oct-26	08-Oct-26	05-Oct-25	06-Oct-25	38,388.86
Catch Basin Sections		97	27-Jun-26 A	12-Nov-26	15-Oct-25	18-Nov-25	249,474.61
CO-R09.S01-SD-	Trench Excavation and Bedding Works for Catch Basins of Storm Drainage Network-	6	27-Jun-26 A	15-Oct-26	15-Oct-25	21-Oct-25	41,579.10
CO-R09.S01-SD-	Installation and Pipes Laying Connection Works for Catch Basins of Storm Drainage	7	29-Jun-26 A	24-Oct-26	22-Oct-25	29-Oct-25	124,737.30
CO-R09.S01-SD-	Trench Backfilling and Compaction Works for Catch Basins of Storm Drainage Netwc	10	03-Aug-26 A	12-Nov-26	08-Nov-25	18-Nov-25	55,438.80
CO-R09.S01-SD-	Testing Works for Catch Basins of Storm Drainage Network-[Road 09] -[SW-1]	7	25-Oct-26	01-Nov-26	30-Oct-25	06-Nov-25	27,719.40
Irrigation Network		7	02-May-26 A	21-Nov-26	09-Dec-25	16-Dec-25	118,783.66
Main Line Pipes		7	02-May-26 A	21-Nov-26	09-Dec-25	16-Dec-25	118,783.66
CO-R09.S01-IR-1	Installation Works for Main Line Valves of Irrigation Network-[Road 09] -[SW-1]	7	02-May-26 A	21-Nov-26	09-Dec-25	16-Dec-25	118,783.66
Medium Voltage Network		4	30-Sep-26 A	23-Jan-27	14-Feb-26	17-Feb-26	138,631.25
Cabling Works		4	30-Sep-26 A	23-Jan-27	14-Feb-26	17-Feb-26	138,631.25
CO-R09.S01-MV-	Trench Excavation and Bedding Works for Medium Voltage Network-[Road 09] -[SW	4	30-Sep-26 A	23-Jan-27	14-Feb-26	17-Feb-26	138,631.25
Road Works		153	10-Jun-26 A	31-Jul-27	21-Jun-26	24-Sep-26	738,543.31
Pre-Bituminous Construction		21	10-Jun-26 A	20-Apr-27	21-Jun-26	14-Jul-26	524,763.79
CO-R09.S01-RD-	Capping and Subgrade Layer for Road Works-[Road 09] -[SW-1]	21	10-Jun-26 A	20-Apr-27	21-Jun-26	14-Jul-26	524,763.79
Pavement Works		12	25-Aug-26 A	31-Jul-27	09-Sep-26	24-Sep-26	213,779.51
CO-R09.S01-RD-	Fixing of Interlock Tiles for Sidewalks Pavement-[Road 09] -[SW-1]	12	25-Aug-26 A	31-Jul-27	09-Sep-26	24-Sep-26	213,779.51
SW_2		494	10-Nov-25 A	07-Aug-27	21-Jul-25	01-Oct-26	1,031,702.30
Sewage Network		279	10-Nov-25 A	26-Oct-26	21-Jul-25	31-Aug-25	289,558.47
Main Line Sections		175	10-Nov-25 A	26-Oct-26	21-Jul-25	31-Aug-25	284,501.38
CO-R09.S02-SW-	Trench Excavation and Bedding Works for Main Lines of Sewage Network-[Road 09]	12	10-Nov-25 A	10-Oct-26	21-Jul-25	03-Aug-25	63,214.65
CO-R09.S02-SW-	Pipes Laying Works for Main Lines of Sewage Network-[Road 09]-[SW-2]	12	15-Feb-26 A	18-Oct-26	04-Aug-25	17-Aug-25	189,643.95
CO-R09.S02-SW-	Trench Backfilling and Compaction Works for Main Lines of Sewage Network-[Road (	12	02-May-26 A	26-Oct-26	18-Aug-25	31-Aug-25	31,642.78
Manholes		1	11-Oct-26	11-Oct-26	25-Aug-25	25-Aug-25	5,057.09
CO-R09.S02-SW-	Testing Works for Main Line Manholes of Sewage Network-[Road 09]-[SW-2]	1	11-Oct-26	11-Oct-26	25-Aug-25	25-Aug-25	5,057.09
Storm Drainage Network		26	22-Jan-26 A	29-Nov-26	16-Oct-25	20-Dec-25	273,456.64

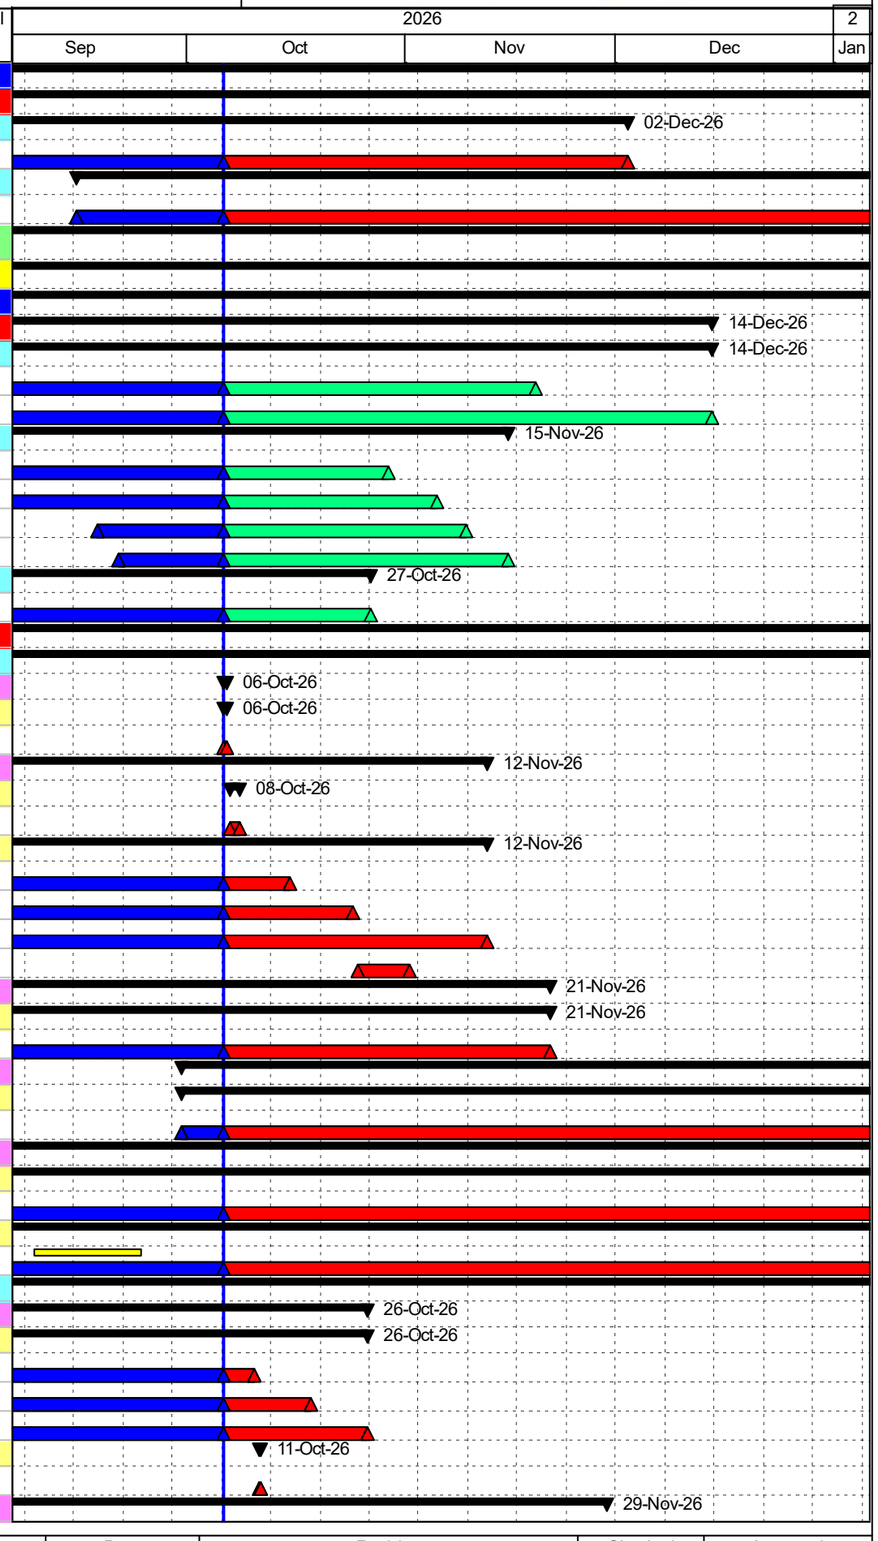


Primary Baseline · Remaining Work · Critical Remaining Work · Actual Work · Baseline Milestone · Milestone · Summary

Date	Revision	Checked	Approved
06-Oct-26	Third Industrial City		

Infrastructure Works of Area J -3rd Industrial City-Dammam-Phase 2 - Part 2 Update 06/10/2026

3Week Lookahead Schedule

Activity ID	Activity Name	Original Duration	Start	Finish	BL Project Start	BL Project Finish	Budgeted Total Cost
Main Line Sections		15	22-Jan-26 A	16-Nov-26	16-Oct-25	02-Nov-25	51,701.44
CO-R09.S02-SD-	Trench Backfilling and Compaction Works for Main Lines of Storm Drainage Network	15	22-Jan-26 A	16-Nov-26	16-Oct-25	02-Nov-25	51,701.44
Catch Basin Sections		24	24-Jun-26 A	29-Nov-26	03-Nov-25	20-Dec-25	221,755.21
CO-R09.S02-SD-	Trench Excavation and Bedding Works for Catch Basins of Storm Drainage Network-	6	24-Jun-26 A	08-Nov-26	03-Nov-25	09-Nov-25	41,579.10
CO-R09.S02-SD-	Installation and Pipes Laying Connection Works for Catch Basins of Storm Drainage	7	25-Jun-26 A	16-Nov-26	30-Nov-25	07-Dec-25	124,737.30
CO-R09.S02-SD-	Trench Backfilling and Compaction Works for Catch Basins of Storm Drainage Netwc	7	28-Jun-26 A	29-Nov-26	13-Dec-25	20-Dec-25	55,438.80
Potable Water Network		53	27-Jun-26 A	17-Jan-27	03-Nov-25	29-Dec-25	254,907.68
Main Line Sections		53	27-Jun-26 A	17-Jan-27	03-Nov-25	29-Dec-25	254,907.68
CO-R09.S02-PW-	Trench Excavation and Bedding Works for Main Lines of Potable Water Network-[Ro	7	27-Jun-26 A	24-Nov-26	03-Nov-25	10-Nov-25	78,463.98
CO-R09.S02-PW-	Pipes Laying and accessories for Main Lines of Potable Water Network-[Road 09]-[	8	30-Jun-26 A	07-Jan-27	10-Dec-25	18-Dec-25	96,160.67
CO-R09.S02-PW-	Trench Backfilling and Compaction Works for Main Lines of Potable Water Network-[I	8	01-Jul-26 A	17-Jan-27	21-Dec-25	29-Dec-25	80,283.03
Road Works		18	25-Aug-26 A	07-Aug-27	09-Sep-26	01-Oct-26	213,779.51
Pavement Works		18	25-Aug-26 A	07-Aug-27	09-Sep-26	01-Oct-26	213,779.51
CO-R09.S02-RD-	Fixing of Interlock Tiles for Sidewalks Pavement-[Road 09]-[SW-2]	18	25-Aug-26 A	07-Aug-27	09-Sep-26	01-Oct-26	213,779.51
Road 10 Local 2 (2352 LM)		256	17-Jun-26 A	21-Jun-27	23-Jul-25	01-Oct-26	2,388,014.23
SW-3		195	25-Aug-26 A	19-Jun-27	09-Sep-25	29-Sep-26	1,008,034.97
SW_3-East		195	25-Aug-26 A	19-Jun-27	09-Sep-25	29-Sep-26	459,218.65
Storm Drainage Network		10	15-Sep-26 A	17-Oct-26	09-Sep-25	15-Oct-25	34,250.86
Manholes		1	15-Sep-26 A	06-Oct-26	09-Sep-25	09-Sep-25	20,352.09
CO-R10.S03-ES	Testing Works for Manholes of Storm Drainage Network-[Road 10]-[SW-3]	1	15-Sep-26 A	06-Oct-26	09-Sep-25	09-Sep-25	20,352.09
Catch Basin Sections		10	15-Sep-26 A	17-Oct-26	05-Oct-25	15-Oct-25	13,898.77
CO-R10.S03-ES	Testing Works for Catch Basins of Storm Drainage Network-[Road 10]-[SW-3]	10	15-Sep-26 A	17-Oct-26	05-Oct-25	15-Oct-25	13,898.77
Potable Water Network		15	06-Oct-26	22-Oct-26	19-Oct-25	04-Nov-25	56,807.63
Fire Hydrant		15	06-Oct-26	22-Oct-26	19-Oct-25	04-Nov-25	56,807.63
CO-R10.S03-ES	Excavation Works for Fire Hydrants of Potable Water Network-[Road 10]-[SW-3]	6	06-Oct-26	12-Oct-26	19-Oct-25	25-Oct-25	8,521.14
CO-R10.S03-ES	Installation Works for Fire Hydrant of Potable Water Network-[Road 10]-[SW-3]	6	13-Oct-26	19-Oct-26	26-Oct-25	01-Nov-25	36,924.96
CO-R10.S03-ES	Trench Backfilling and Compaction Works for Fire Hydrants of Potable Water Networl	6	17-Oct-26	22-Oct-26	29-Oct-25	04-Nov-25	11,361.53
Street Lighting Network		33	06-Oct-26	12-Nov-26	02-Dec-25	16-Feb-26	59,653.58
Lighting Poles Works		33	06-Oct-26	12-Nov-26	02-Dec-25	16-Feb-26	59,653.58
CO-R10.S03-ES	Foundation Excavation Works for Lighting Poles of Street Lighting Network-[Road 10	12	06-Oct-26	19-Oct-26	02-Dec-25	15-Dec-25	2,284.16
CO-R10.S03-ES	Installation Works for Lighting Poles Foundation of Street Lighting Network-[Road 10	12	12-Oct-26	25-Oct-26	08-Dec-25	21-Dec-25	8,731.44
CO-R10.S03-ES	Installation Works for Lighting Poles of Street Lighting Network-[Road 10]-[SW-3]	18	18-Oct-26	07-Nov-26	14-Dec-25	03-Jan-26	25,125.80
CO-R10.S03-ES	Installation Works for Lighting Fixtures With Drop Wire of Street Lighting Network-[Rc	18	24-Oct-26	12-Nov-26	26-Jan-26	16-Feb-26	14,375.52
CO-R10.S03-ES	Backfilling Works for Lighting Poles of Street Lighting Network-[Road 10]-[SW-3]	12	25-Oct-26	07-Nov-26	27-Jan-26	10-Feb-26	9,136.66
Medium Voltage Network		24	09-Sep-26 A	25-Jan-27	24-Feb-26	26-Mar-26	201,322.52
Cabling Works		24	09-Sep-26 A	25-Jan-27	24-Feb-26	26-Mar-26	201,322.52
CO-R10.S03-ES	Trench Excavation and Bedding Works for Medium Voltage Network-[Road 10]-[SW-	18	09-Sep-26 A	18-Jan-27	24-Feb-26	16-Mar-26	23,183.87
CO-R10.S03-ES	Cable Laying Works for Medium Voltage Network-[Road 10]-[SW-3]	18	13-Sep-26 A	21-Jan-27	28-Feb-26	19-Mar-26	124,697.05
CO-R10.S03-ES	Trench Backfilling and Compaction Works for Medium Voltage Network-[Road 10]-[S	18	16-Sep-26 A	25-Jan-27	03-Mar-26	26-Mar-26	53,441.59
Road Works		10	25-Aug-26 A	19-Jun-27	17-Sep-26	29-Sep-26	107,184.05
Pavement Works		10	25-Aug-26 A	19-Jun-27	17-Sep-26	29-Sep-26	107,184.05
CO-R10.S03-ES	Fixing of Interlock Tiles for Sidewalks Pavement-[Road 10]-[SW-3]	10	25-Aug-26 A	19-Jun-27	17-Sep-26	29-Sep-26	107,184.05
SW_3-West		178	25-Aug-26 A	19-Jun-27	07-Dec-25	29-Sep-26	548,816.32
Storm Drainage Network		10	06-Oct-26	17-Oct-26	07-Dec-25	11-Jan-26	38,636.01
Manholes		1	06-Oct-26	06-Oct-26	07-Dec-25	07-Dec-25	24,737.24
CO-R10.S03-WE	Testing Works for Manholes of Storm Drainage Network-[Road 10]-[SW-3]	1	06-Oct-26	06-Oct-26	07-Dec-25	07-Dec-25	24,737.24
Catch Basin Sections		10	06-Oct-26	17-Oct-26	31-Dec-25	11-Jan-26	13,898.77
CO-R10.S03-WE	Testing Works for Catch Basins of Storm Drainage Network-[Road 10]-[SW-3]	10	06-Oct-26	17-Oct-26	31-Dec-25	11-Jan-26	13,898.77
Potable Water Network		16	06-Oct-26	24-Oct-26	05-Jan-26	25-Jan-26	142,020.14
Valve Chamber		16	06-Oct-26	24-Oct-26	05-Jan-26	22-Jan-26	85,212.52
CO-R10.S03-WE	Excavation Works for Main Line Valves and Valve Chambers of Potable Water Netwc	1	06-Oct-26	06-Oct-26	05-Jan-26	05-Jan-26	4,352.45
CO-R10.S03-WE	RC Footing Works for Main Line Valves and Valve Chambers of Potable Water Netv	3	07-Oct-26	10-Oct-26	06-Jan-26	08-Jan-26	6,528.67
CO-R10.S03-WE	RC Wall Works for Main Line Valves and Valve Chambers of Potable Water Network	6	11-Oct-26	17-Oct-26	10-Jan-26	15-Jan-26	15,233.56

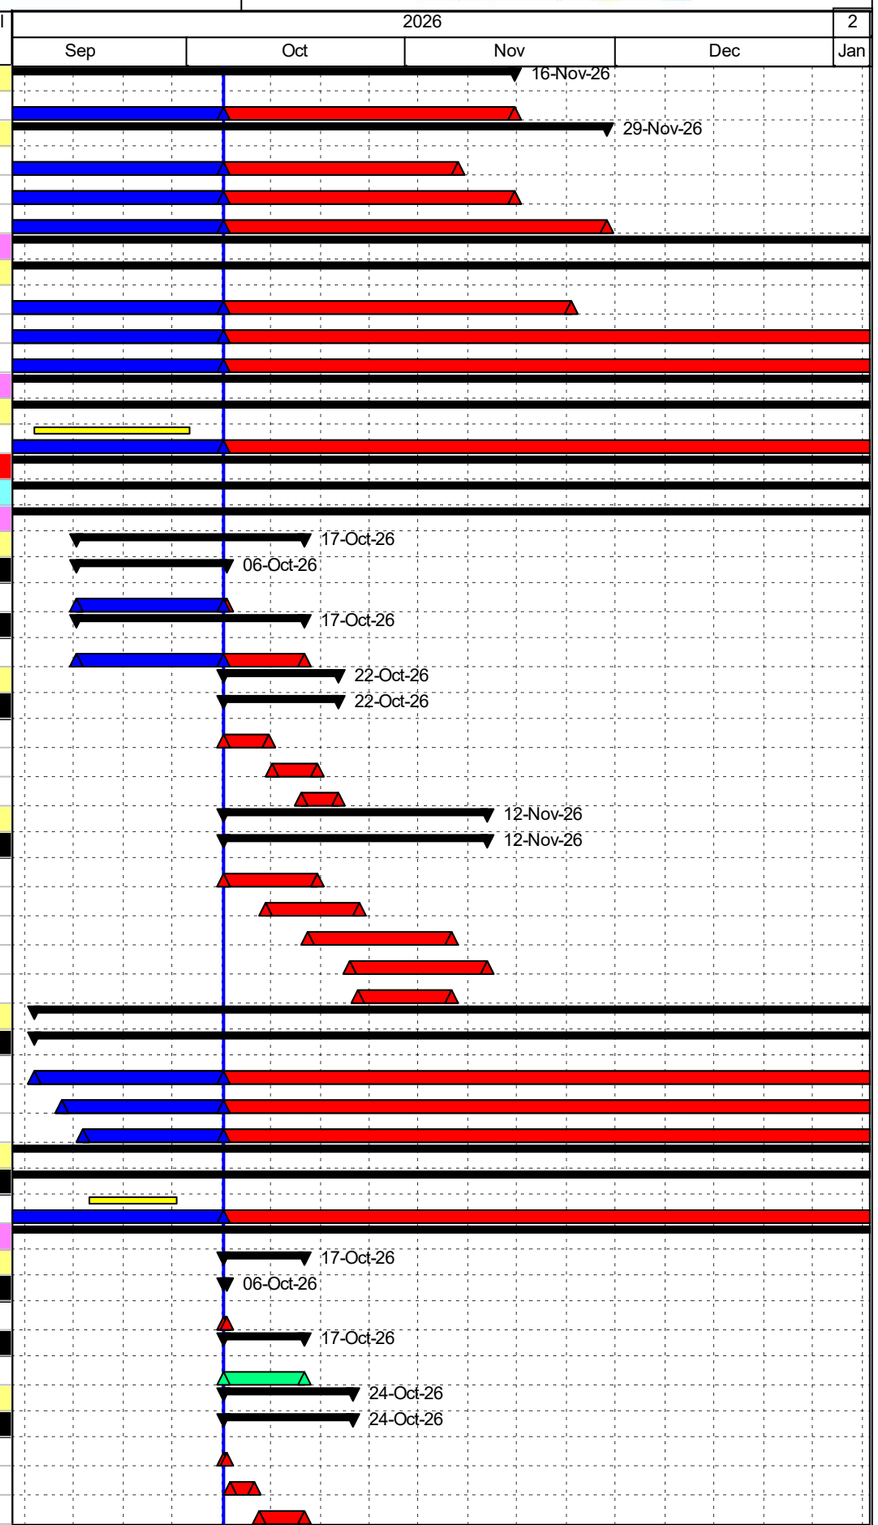


Primary Baseline | Actual Work | Summary
Remaining Work | Baseline Milestone
Critical Remaining Work | Milestone

Date	Revision	Checked	Approved
06-Oct-26	Third Industrial City		

Infrastructure Works of Area J -3rd Industrial City-
Dammam-Phase 2 - Part 2 Update 06/10/2026
3Week Lookahead Schedule

Activity ID	Activity Name	Original Duration	Start	Finish	BL Project Start	BL Project Finish	Budgeted Total Cost
CO-R10.S03-WE	RC Slab Works for Main Line Valves and Valve Chambers of Potable Water Networl	2	18-Oct-26	19-Oct-26	17-Jan-26	18-Jan-26	8,704.89
CO-R10.S03-WE	Insulation Works for Main Line Valves and Valve Chambers of Potable Water Netwo	1	20-Oct-26	20-Oct-26	19-Jan-26	19-Jan-26	41,688.07
CO-R10.S03-WE	Backfilling Works for Main Line Valves and Valve Chambers of Potable Water Netwo	3	21-Oct-26	24-Oct-26	20-Jan-26	22-Jan-26	8,704.89
Fire Hydrant		15	06-Oct-26	22-Oct-26	08-Jan-26	25-Jan-26	56,807.63
CO-R10.S03-WE	Excavation Works for Fire Hydrants of Potable Water Network-[Road 10]-[SW-3]	6	06-Oct-26	12-Oct-26	08-Jan-26	14-Jan-26	8,521.14
CO-R10.S03-WE	Installation Works for Fire Hydrant of Potable Water Network-[Road 10]-[SW-3]	6	13-Oct-26	19-Oct-26	15-Jan-26	21-Jan-26	36,924.96
CO-R10.S03-WE	Trench Backfilling and Compaction Works for Fire Hydrants of Potable Water Networl	6	17-Oct-26	22-Oct-26	19-Jan-26	25-Jan-26	11,361.53
Street Lighting Network		33	06-Oct-26	12-Nov-26	22-Feb-26	04-Apr-26	59,653.58
Lighting Poles Works		33	06-Oct-26	12-Nov-26	22-Feb-26	04-Apr-26	59,653.58
CO-R10.S03-WE	Foundation Excavation Works for Lighting Poles of Street Lighting Network-[Road 10	12	06-Oct-26	19-Oct-26	22-Feb-26	07-Mar-26	2,284.16
CO-R10.S03-WE	Installation Works for Lighting Poles Foundation of Street Lighting Network-[Road 10	12	12-Oct-26	25-Oct-26	28-Feb-26	12-Mar-26	8,731.44
CO-R10.S03-WE	Installation Works for Lighting Poles of Street Lighting Network-[Road 10]-[SW-3]	18	18-Oct-26	07-Nov-26	05-Mar-26	29-Mar-26	25,125.80
CO-R10.S03-WE	Installation Works for Lighting Fixtures With Drop Wire of Street Lighting Network-[Rc	18	24-Oct-26	12-Nov-26	11-Mar-26	04-Apr-26	14,375.52
CO-R10.S03-WE	Backfilling Works for Lighting Poles of Street Lighting Network-[Road 10]-[SW-3]	12	25-Oct-26	07-Nov-26	12-Mar-26	29-Mar-26	9,136.66
Medium Voltage Network		16	22-Sep-26 A	18-Apr-27	11-Jul-26	28-Jul-26	201,322.52
Cabling Works		16	22-Sep-26 A	18-Apr-27	11-Jul-26	28-Jul-26	201,322.52
CO-R10.S03-WE	Trench Excavation and Bedding Works for Medium Voltage Network-[Road 10]-[SW-	10	22-Sep-26 A	11-Apr-27	11-Jul-26	21-Jul-26	23,183.87
CO-R10.S03-WE	Cable Laying Works for Medium Voltage Network-[Road 10]-[SW-3]	10	22-Sep-26 A	14-Apr-27	14-Jul-26	25-Jul-26	124,697.05
CO-R10.S03-WE	Trench Backfilling and Compaction Works for Medium Voltage Network-[Road 10]-[S	10	22-Sep-26 A	18-Apr-27	18-Jul-26	28-Jul-26	53,441.59
Road Works		10	25-Aug-26 A	19-Jun-27	17-Sep-26	29-Sep-26	107,184.05
Pavement Works		10	25-Aug-26 A	19-Jun-27	17-Sep-26	29-Sep-26	107,184.05
CO-R10.S03-WE	Fixing of Interlock Tiles for Sidewalks Pavement-[Road 10]-[SW-3]	10	25-Aug-26 A	19-Jun-27	17-Sep-26	29-Sep-26	107,184.05
SW-4		256	17-Jun-26 A	21-Jun-27	23-Jul-25	01-Oct-26	1,379,979.27
SW_4-East		243	21-Jun-26 A	19-Jun-27	23-Jul-25	29-Sep-26	601,912.63
Sewage Network		1	06-Oct-26	06-Oct-26	23-Jul-25	23-Jul-25	8,813.28
Manholes		1	06-Oct-26	06-Oct-26	23-Jul-25	23-Jul-25	8,813.28
CO-R10.S04-ES	Testing Works for Main Line Manholes of Sewage Network-[Road 10]-[SW-4]	1	06-Oct-26	06-Oct-26	23-Jul-25	23-Jul-25	8,813.28
Storm Drainage Network		10	06-Oct-26	17-Oct-26	18-Dec-25	22-Jan-26	34,250.86
Manholes		1	06-Oct-26	06-Oct-26	18-Dec-25	18-Dec-25	20,352.09
CO-R10.S04-ES	Testing Works for Manholes of Storm Drainage Network-[Road 10]-[SW-4]	1	06-Oct-26	06-Oct-26	18-Dec-25	18-Dec-25	20,352.09
Catch Basin Sections		10	06-Oct-26	17-Oct-26	12-Jan-26	22-Jan-26	13,898.77
CO-R10.S04-ES	Testing Works for Catch Basins of Storm Drainage Network-[Road 10]-[SW-4]	10	06-Oct-26	17-Oct-26	12-Jan-26	22-Jan-26	13,898.77
Potable Water Network		81	21-Jun-26 A	24-Oct-26	15-Jan-26	02-Feb-26	451,664.43
Valve Chamber		81	21-Jun-26 A	24-Oct-26	15-Jan-26	02-Feb-26	451,664.43
CO-R10.S04-ES	Insulation Works for Main Line Valves and Valve Chambers of Potable Water Netwo	1	21-Jun-26 A	20-Oct-26	29-Jan-26	29-Jan-26	319,298.55
CO-R10.S04-ES	Excavation Works for Main Line Valves and Valve Chambers of Potable Water Netwo	1	06-Oct-26	06-Oct-26	15-Jan-26	15-Jan-26	16,109.01
CO-R10.S04-ES	RC Footing Works for Main Line Valves and Valve Chambers of Potable Water Netv	3	07-Oct-26	10-Oct-26	17-Jan-26	19-Jan-26	19,376.15
CO-R10.S04-ES	RC Wall Works for Main Line Valves and Valve Chambers of Potable Water Network	6	11-Oct-26	17-Oct-26	20-Jan-26	26-Jan-26	45,211.01
CO-R10.S04-ES	RC Slab Works for Main Line Valves and Valve Chambers of Potable Water Networl	2	18-Oct-26	19-Oct-26	27-Jan-26	28-Jan-26	25,834.86
CO-R10.S04-ES	Backfilling Works for Main Line Valves and Valve Chambers of Potable Water Netwo	3	21-Oct-26	24-Oct-26	31-Jan-26	02-Feb-26	25,834.86
Road Works		10	25-Aug-26 A	19-Jun-27	17-Sep-26	29-Sep-26	107,184.05
Pavement Works		10	25-Aug-26 A	19-Jun-27	17-Sep-26	29-Sep-26	107,184.05
CO-R10.S04-ES	Fixing of Interlock Tiles for Sidewalks Pavement-[Road 10]-[SW-4]	10	25-Aug-26 A	19-Jun-27	17-Sep-26	29-Sep-26	107,184.05
SW_4-West		256	17-Jun-26 A	21-Jun-27	11-Nov-25	01-Oct-26	778,066.64
Sewage Network		1	06-Oct-26	06-Oct-26	11-Nov-25	11-Nov-25	10,264.33
Manholes		1	06-Oct-26	06-Oct-26	11-Nov-25	11-Nov-25	10,264.33
CO-R10.S04-WE	Testing Works for Main Line Manholes of Sewage Network-[Road 10]-[SW-4]	1	06-Oct-26	06-Oct-26	11-Nov-25	11-Nov-25	10,264.33
Storm Drainage Network		88	17-Jun-26 A	19-Oct-26	18-Dec-25	26-Jan-26	147,127.45
Manholes		1	06-Oct-26	06-Oct-26	18-Dec-25	18-Dec-25	22,037.94
CO-R10.S04-WE	Testing Works for Manholes of Storm Drainage Network-[Road 10]-[SW-4]	1	06-Oct-26	06-Oct-26	18-Dec-25	18-Dec-25	22,037.94
Catch Basin Sections		88	17-Jun-26 A	19-Oct-26	28-Dec-25	26-Jan-26	125,089.51
CO-R10.S04-WE	Trench Excavation and Bedding Works for Catch Basins of Storm Drainage Network-	6	17-Jun-26 A	08-Oct-26	28-Dec-25	03-Jan-26	20,848.43
CO-R10.S04-WE	Installation and Pipes Laying Connection Works for Catch Basins of Storm Drainage	7	20-Jun-26 A	11-Oct-26	04-Jan-26	11-Jan-26	62,544.75

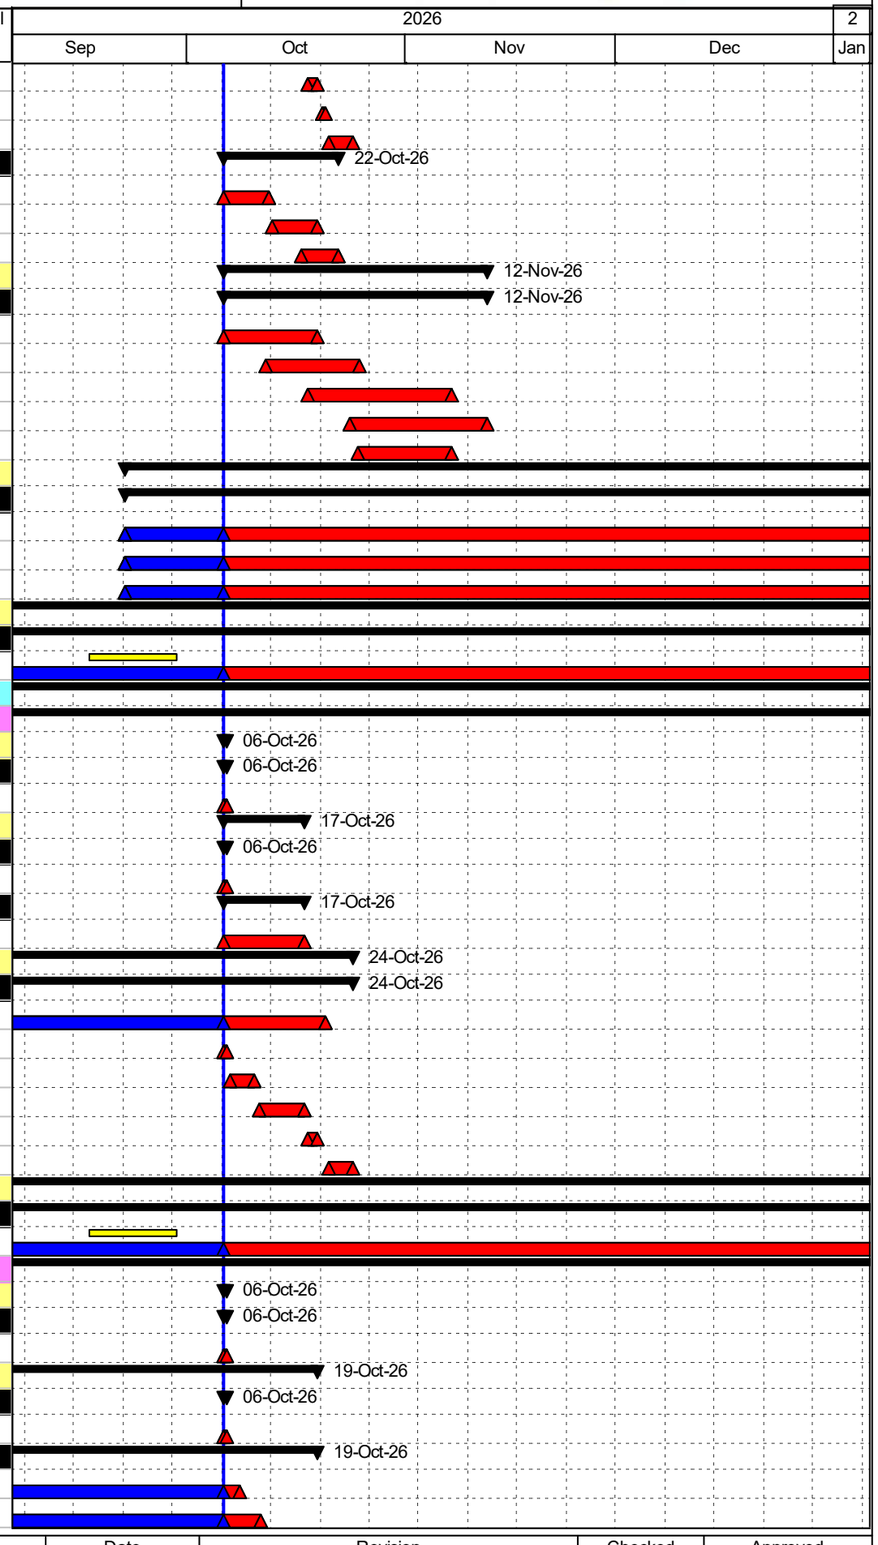


Primary Baseline | Actual Work | Summary
Remaining Work | Baseline Milestone
Critical Remaining Work | Milestone

Date	Revision	Checked	Approved
06-Oct-26	Third Industrial City		

Infrastructure Works of Area J -3rd Industrial City-
Dammam-Phase 2 - Part 2 Update 06/10/2026
3Week Lookahead Schedule

Activity ID	Activity Name	Original Duration	Start	Finish	BL Project Start	BL Project Finish	Budgeted Total Cost
CO-R10.S04-WE	Testing Works for Catch Basins of Storm Drainage Network-[Road 10]-[SW-4]	10	23-Jun-26 A	14-Oct-26	12-Jan-26	22-Jan-26	13,898.77
CO-R10.S04-WE	Trench Backfilling and Compaction Works for Catch Basins of Storm Drainage Netwc	7	12-Oct-26	19-Oct-26	19-Jan-26	26-Jan-26	27,797.55
Potable Water Network		81	21-Jun-26 A	24-Oct-26	15-Jan-26	02-Feb-26	406,090.05
Valve Chamber		81	21-Jun-26 A	24-Oct-26	15-Jan-26	02-Feb-26	406,090.05
CO-R10.S04-WE	Insulation Works for Main Line Valves and Valve Chambers of Potable Water Netwo	1	21-Jun-26 A	20-Oct-26	29-Jan-26	29-Jan-26	319,298.55
CO-R10.S04-WE	Excavation Works for Main Line Valves and Valve Chambers of Potable Water Netwc	1	06-Oct-26	06-Oct-26	15-Jan-26	15-Jan-26	8,679.15
CO-R10.S04-WE	RC Footing Works for Main Line Valves and Valve Chambers of Potable Water Netv	3	07-Oct-26	10-Oct-26	17-Jan-26	19-Jan-26	13,018.73
CO-R10.S04-WE	RC Wall Works for Main Line Valves and Valve Chambers of Potable Water Network	6	11-Oct-26	17-Oct-26	20-Jan-26	26-Jan-26	30,377.03
CO-R10.S04-WE	RC Slab Works for Main Line Valves and Valve Chambers of Potable Water Networl	2	18-Oct-26	19-Oct-26	27-Jan-26	28-Jan-26	17,358.30
CO-R10.S04-WE	Backfilling Works for Main Line Valves and Valve Chambers of Potable Water Netwo	3	21-Oct-26	24-Oct-26	31-Jan-26	02-Feb-26	17,358.30
Irrigation Network		20	06-Oct-26	28-Oct-26	12-Feb-26	02-Mar-26	107,400.75
Main Line Pipes		20	06-Oct-26	28-Oct-26	12-Feb-26	02-Mar-26	107,400.75
CO-R10.S04-WE	Trench Excavation and Bedding Works for Main Lines of Irrigation Network-[Road 10	6	06-Oct-26	12-Oct-26	12-Feb-26	18-Feb-26	21,371.93
CO-R10.S04-WE	Pipes Laying Works for Main Lines of Irrigation Network-[Road 10]-[SW-4]	7	13-Oct-26	20-Oct-26	19-Feb-26	26-Feb-26	64,103.07
CO-R10.S04-WE	Installation Works for Main Line Valves of Irrigation Network-[Road 10]-[SW-4]	3	26-Oct-26	28-Oct-26	28-Feb-26	02-Mar-26	21,925.75
Road Works		12	25-Aug-26 A	21-Jun-27	17-Sep-26	01-Oct-26	107,184.05
Pavement Works		12	25-Aug-26 A	21-Jun-27	17-Sep-26	01-Oct-26	107,184.05
CO-R10.S04-WE	Fixing of Interlock Tiles for Sidewalks Pavement-[Road 10]-[SW-4]	12	25-Aug-26 A	21-Jun-27	17-Sep-26	01-Oct-26	107,184.05
Road 11 Local 1 (670 LM)		361	02-Apr-26 A	31-Jul-27	04-Oct-25	13-Oct-26	281,642.20
SW_5		273	25-Apr-26 A	31-Jul-27	03-Jan-26	11-Oct-26	99,873.04
Irrigation Network		7	25-Apr-26 A	09-Nov-26	03-Jan-26	10-Jan-26	37,411.08
Main Line Pipes		7	25-Apr-26 A	09-Nov-26	03-Jan-26	10-Jan-26	37,411.08
CO-R11.S05-IR-1	Pipes Laying Works for Main Lines of Irrigation Network-[Road 11]-[SW-5]	7	25-Apr-26 A	09-Nov-26	03-Jan-26	10-Jan-26	37,411.08
Road Works		10	25-Aug-26 A	31-Jul-27	30-Sep-26	11-Oct-26	62,461.96
Pavement Works		10	25-Aug-26 A	31-Jul-27	30-Sep-26	11-Oct-26	62,461.96
CO-R11.S05-RD-	Fixing of Interlock Tiles for Sidewalks Pavement-[Road 11]-[SW-5]	10	25-Aug-26 A	31-Jul-27	30-Sep-26	11-Oct-26	62,461.96
SW_6		287	02-Apr-26 A	31-Jul-27	04-Oct-25	13-Oct-26	181,769.16
Sewage Network		147	02-Apr-26 A	11-Oct-26	04-Oct-25	14-Oct-25	81,435.45
Manholes		147	02-Apr-26 A	11-Oct-26	04-Oct-25	14-Oct-25	81,435.45
CO-R11.S06-SW-	Install Grp Liner Wall Works for Main Line Manholes of Sewage Network-[Road 11]-[S	4	02-Apr-26 A	10-Oct-26	04-Oct-25	07-Oct-25	72,387.07
CO-R11.S06-SW-	Testing Works for Main Line Manholes of Sewage Network-[Road 11]-[SW-6]	1	11-Oct-26	11-Oct-26	14-Oct-25	14-Oct-25	9,048.38
Potable Water Network		21	06-Oct-26	29-Oct-26	04-Feb-26	28-Feb-26	37,871.75
Fire Hydrant		21	06-Oct-26	29-Oct-26	04-Feb-26	28-Feb-26	37,871.75
CO-R11.S06-PW-	Excavation Works for Fire Hydrants of Potable Water Network-[Road 11]-[SW-6]	7	06-Oct-26	13-Oct-26	04-Feb-26	11-Feb-26	5,680.76
CO-R11.S06-PW-	Installation Works for Fire Hydrant of Potable Water Network-[Road 11]-[SW-6]	7	14-Oct-26	21-Oct-26	12-Feb-26	19-Feb-26	24,616.64
CO-R11.S06-PW-	Trench Backfilling and Compaction Works for Fire Hydrants of Potable Water Networl	7	22-Oct-26	29-Oct-26	21-Feb-26	28-Feb-26	7,574.35
Road Works		10	25-Aug-26 A	31-Jul-27	03-Oct-26	13-Oct-26	62,461.96
Pavement Works		10	25-Aug-26 A	31-Jul-27	03-Oct-26	13-Oct-26	62,461.96
CO-R11.S06-RD-	Fixing of Interlock Tiles for Sidewalks Pavement-[Road 11]-[SW-6]	10	25-Aug-26 A	31-Jul-27	03-Oct-26	13-Oct-26	62,461.96
Road 14 Local 1 (584 LM)		233	25-Aug-26 A	14-Aug-27	05-Aug-25	27-Oct-26	246,536.62
SW_7		233	25-Aug-26 A	14-Aug-27	05-Aug-25	25-Oct-26	98,746.88
Sewage Network		1	06-Oct-26	06-Oct-26	01-Sep-25	01-Sep-25	6,319.37
Manholes		1	06-Oct-26	06-Oct-26	01-Sep-25	01-Sep-25	6,319.37
CO-R14.S07-SW-	Testing Works for Main Line Manholes of Sewage Network-[Road 14]-[SW-7]	1	06-Oct-26	06-Oct-26	01-Sep-25	01-Sep-25	6,319.37
Street Lighting Network		24	06-Oct-26	02-Nov-26	05-Aug-25	28-Aug-25	0.00
Distrubution Panel Boards		24	06-Oct-26	02-Nov-26	05-Aug-25	28-Aug-25	0.00
salman	Foundation Excavation Works For Panel Boards of Street Lighting Network-[Road 14	18	06-Oct-26	26-Oct-26			0.00
CO-R14.S07-SL-	Installation Works for Panel Board Concrete Foundations of Street Lighting Network-	18	10-Oct-26	29-Oct-26	05-Aug-25	25-Aug-25	0.00
CO-R14.S07-SL-	A wall of concrete blocks to install the KWH meter of Street Lighting Network-[Road 1	18	10-Oct-26	29-Oct-26	05-Aug-25	25-Aug-25	0.00
CO-R14.S07-SL-	Installation Works for Lighting Panel Boards of Street Lighting Network-[Road 14]-[S\	18	13-Oct-26	02-Nov-26	09-Aug-25	28-Aug-25	0.00
Road Works		12	25-Aug-26 A	14-Aug-27	12-Oct-26	25-Oct-26	92,427.51
Pavement Works		12	25-Aug-26 A	14-Aug-27	12-Oct-26	25-Oct-26	92,427.51
CO-R14.S07-RD-	Fixing of Interlock Tiles for Sidewalks Pavement-[Road 14]-[SW-7]	12	25-Aug-26 A	14-Aug-27	12-Oct-26	25-Oct-26	92,427.51

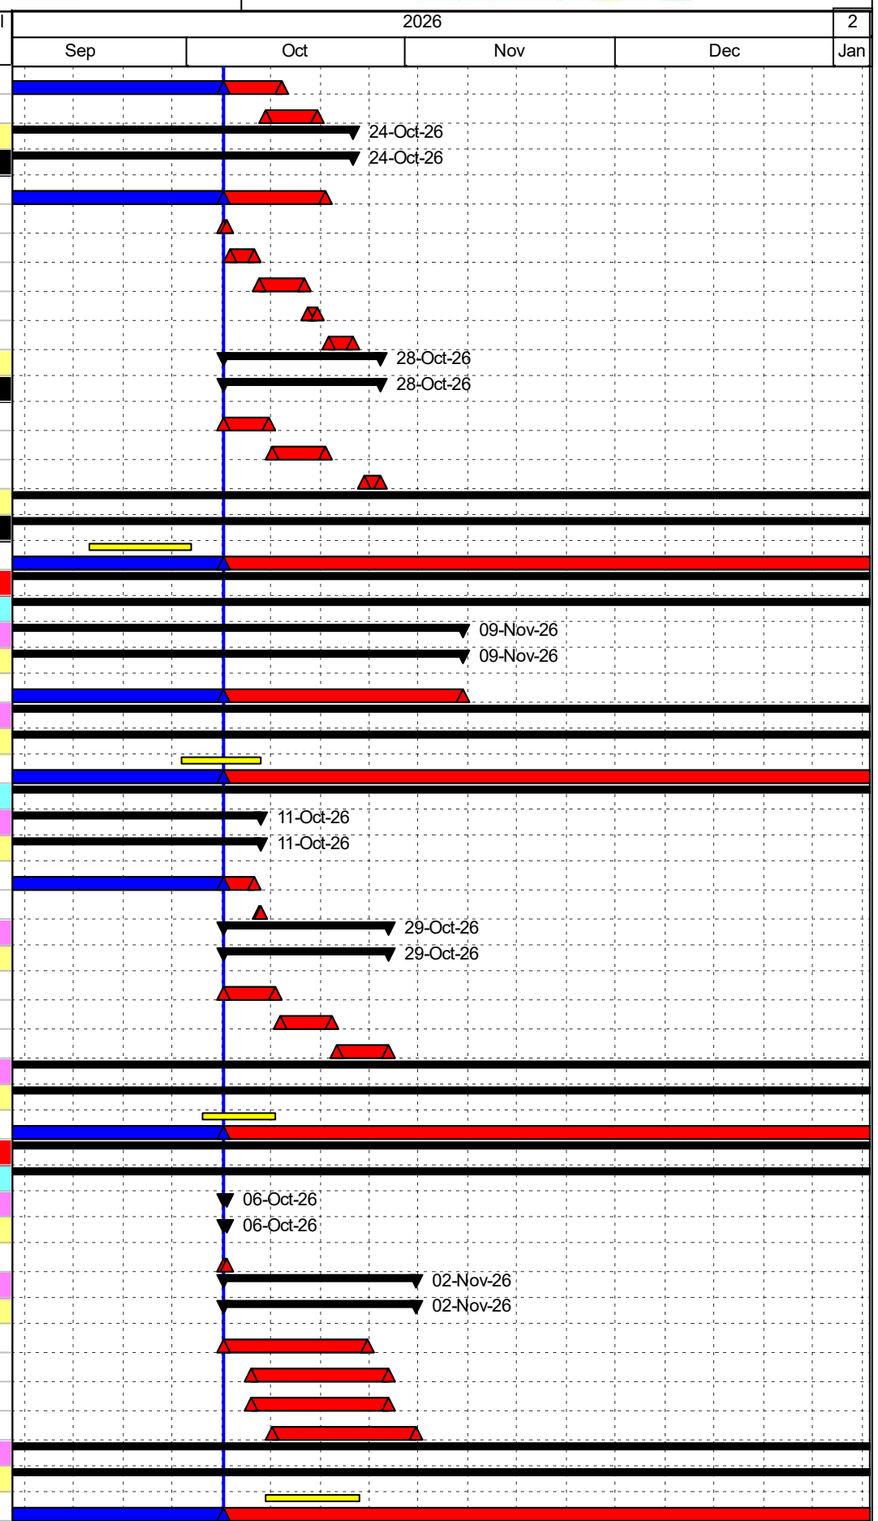


Primary Baseline | Actual Work | Summary
Remaining Work | Baseline Milestone
Critical Remaining Work | Milestone

Date	Revision	Checked	Approved
06-Oct-26	Third Industrial City		

Infrastructure Works of Area J -3rd Industrial City-
Dammam-Phase 2 - Part 2 Update 06/10/2026
3Week Lookahead Schedule

Activity ID	Activity Name	Original Duration	Start	Finish	BL Project Start	BL Project Finish	Budgeted Total Cost
SW_8		233	25-Aug-26 A	14-Aug-27	15-Sep-25	27-Oct-26	147,789.74
Sewage Network		1	06-Oct-26	06-Oct-26	15-Sep-25	15-Sep-25	2,341.78
Manholes		1	06-Oct-26	06-Oct-26	15-Sep-25	15-Sep-25	2,341.78
CO-R14.S08-SW-	Testing Works for Main Line Manholes of Sewage Network-[Road 14]-[SW-8]	1	06-Oct-26	06-Oct-26	15-Sep-25	15-Sep-25	2,341.78
Potable Water Network		21	06-Oct-26	29-Oct-26	26-Feb-26	25-Mar-26	53,020.45
Fire Hydrant		21	06-Oct-26	29-Oct-26	26-Feb-26	25-Mar-26	53,020.45
CO-R14.S08-PW-	Excavation Works for Fire Hydrants of Potable Water Network-[Road 14]-[SW-8]	7	06-Oct-26	13-Oct-26	26-Feb-26	05-Mar-26	7,953.07
CO-R14.S08-PW-	Installation Works for Fire Hydrant of Potable Water Network-[Road 14]-[SW-8]	7	14-Oct-26	21-Oct-26	07-Mar-26	14-Mar-26	34,463.29
CO-R14.S08-PW-	Trench Backfilling and Compaction Works for Fire Hydrants of Potable Water Networl	7	22-Oct-26	29-Oct-26	15-Mar-26	25-Mar-26	10,604.09
Road Works		12	25-Aug-26 A	14-Aug-27	14-Oct-26	27-Oct-26	92,427.51
Pavement Works		12	25-Aug-26 A	14-Aug-27	14-Oct-26	27-Oct-26	92,427.51
CO-R14.S08-RD-	Fixing of Interlock Tiles for Sidewalks Pavement-[Road 14]-[SW-8]	12	25-Aug-26 A	14-Aug-27	14-Oct-26	27-Oct-26	92,427.51
Road 15 Local 1 (556 LM)		247	25-Aug-26 A	28-Aug-27	02-Jun-25	08-Nov-26	165,085.56
SW_9		12	25-Aug-26 A	28-Aug-27	26-Oct-26	08-Nov-26	52,781.33
Road Works		12	25-Aug-26 A	28-Aug-27	26-Oct-26	08-Nov-26	52,781.33
Pavement Works		12	25-Aug-26 A	28-Aug-27	26-Oct-26	08-Nov-26	52,781.33
CO-R15.S09-RD-	Fixing of Interlock Tiles for Sidewalks Pavement-[Road 15]-[SW-9]	12	25-Aug-26 A	28-Aug-27	26-Oct-26	08-Nov-26	52,781.33
SW_10		245	25-Aug-26 A	25-Aug-27	02-Jun-25	08-Nov-26	112,304.23
Sewage Network		1	06-Oct-26	06-Oct-26	05-Jul-25	06-Jul-25	2,882.74
Manholes		1	06-Oct-26	06-Oct-26	05-Jul-25	06-Jul-25	2,882.74
CO-R15.S10-SW-	Testing Works for Main Line Manholes of Sewage Network-[Road 15]-[SW-10]	1	06-Oct-26	06-Oct-26	05-Jul-25	06-Jul-25	2,882.74
Street Lighting Network		24	06-Oct-26	02-Nov-26	02-Jun-25	02-Feb-26	26,342.77
Lighting Poles Works		5	06-Oct-26	11-Oct-26	27-Jan-26	02-Feb-26	9,517.35
CO-R15.S10-SL-;	Testing Works for Lighting Poles of Street Lighting Network-[Road 15]-[SW-10]	5	06-Oct-26	11-Oct-26	27-Jan-26	02-Feb-26	9,517.35
Distrubution Panel Boards		24	06-Oct-26	02-Nov-26	02-Jun-25	03-Jul-25	16,825.42
CO-R15.S10-SL-'	Foundation Excavation Works For Panel Boards of Street Lighting Network-[Road 15	18	06-Oct-26	26-Oct-26	02-Jun-25	26-Jun-25	0.00
CO-R15.S10-SL-'	Installation Works for Panel Board Concrete Foundations of Street Lighting Network-	18	10-Oct-26	29-Oct-26	10-Jun-25	30-Jun-25	0.00
CO-R15.S10-SL-;	A wall of concrete blocks to install the KWH meter of Street Lighting Network-[Road 1	18	10-Oct-26	29-Oct-26	10-Jun-25	30-Jun-25	16,825.42
CO-R15.S10-SL-'	Installation Works for Lighting Panel Boards of Street Lighting Network-[Road 15]-[S\	18	13-Oct-26	02-Nov-26	14-Jun-25	03-Jul-25	0.00
Potable Water Network		18	06-Oct-26	26-Oct-26	08-Mar-26	31-Mar-26	30,297.40
Fire Hydrant		18	06-Oct-26	26-Oct-26	08-Mar-26	31-Mar-26	30,297.40
CO-R15.S10-PW-	Excavation Works for Fire Hydrants of Potable Water Network-[Road 15]-[SW-10]	6	06-Oct-26	12-Oct-26	08-Mar-26	14-Mar-26	4,544.61
CO-R15.S10-PW-	Installation Works for Fire Hydrant of Potable Water Network-[Road 15]-[SW-10]	6	13-Oct-26	19-Oct-26	15-Mar-26	24-Mar-26	19,693.31
CO-R15.S10-PW-	Trench Backfilling and Compaction Works for Fire Hydrants of Potable Water Networl	6	20-Oct-26	26-Oct-26	25-Mar-26	31-Mar-26	6,059.48
Road Works		10	25-Aug-26 A	25-Aug-27	28-Oct-26	08-Nov-26	52,781.33
Pavement Works		10	25-Aug-26 A	25-Aug-27	28-Oct-26	08-Nov-26	52,781.33
CO-R15.S10-RD-	Fixing of Interlock Tiles for Sidewalks Pavement-[Road 15]-[SW-10]	10	25-Aug-26 A	25-Aug-27	28-Oct-26	08-Nov-26	52,781.33
Road 16 Local 1 (527 LM)		257	25-Aug-26 A	06-Sep-27	29-Mar-26	19-Nov-26	124,973.63
SW_11		10	25-Aug-26 A	25-Aug-27	05-Nov-26	16-Nov-26	50,367.85
Road Works		10	25-Aug-26 A	25-Aug-27	05-Nov-26	16-Nov-26	50,367.85
Pavement Works		10	25-Aug-26 A	25-Aug-27	05-Nov-26	16-Nov-26	50,367.85
CO-R16.S11-RD-	Fixing of Interlock Tiles for Sidewalks Pavement-[Road 16]-[SW-11]	10	25-Aug-26 A	25-Aug-27	05-Nov-26	16-Nov-26	50,367.85
SW_12		257	25-Aug-26 A	06-Sep-27	29-Mar-26	19-Nov-26	74,605.77
Potable Water Network		18	06-Oct-26	26-Oct-26	29-Mar-26	11-Apr-26	24,237.92
Fire Hydrant		18	06-Oct-26	26-Oct-26	29-Mar-26	11-Apr-26	24,237.92
CO-R16.S12-PW-	Excavation Works for Fire Hydrants of Potable Water Network-[Road 16]-[SW-12]	6	06-Oct-26	12-Oct-26	29-Mar-26	04-Apr-26	4,544.61
CO-R16.S12-PW-	Installation Works for Fire Hydrant of Potable Water Network-[Road 16]-[SW-12]	6	20-Oct-26	26-Oct-26	05-Apr-26	11-Apr-26	19,693.31
Road Works		10	25-Aug-26 A	06-Sep-27	09-Nov-26	19-Nov-26	50,367.85
Pavement Works		10	25-Aug-26 A	06-Sep-27	09-Nov-26	19-Nov-26	50,367.85
CO-R16.S12-RD-	Fixing of Interlock Tiles for Sidewalks Pavement-[Road 16]-[SW-12]	10	25-Aug-26 A	06-Sep-27	09-Nov-26	19-Nov-26	50,367.85
Road 17 Local 1 (500 LM)		24	06-Oct-26	02-Nov-26	16-Apr-25	01-Sep-26	55,888.95
SW_14		24	06-Oct-26	02-Nov-26	16-Apr-25	01-Sep-26	55,888.95
Sewage Network		1	06-Oct-26	06-Oct-26	21-May-25	21-May-25	1,517.62
Manholes		1	06-Oct-26	06-Oct-26	21-May-25	21-May-25	1,517.62

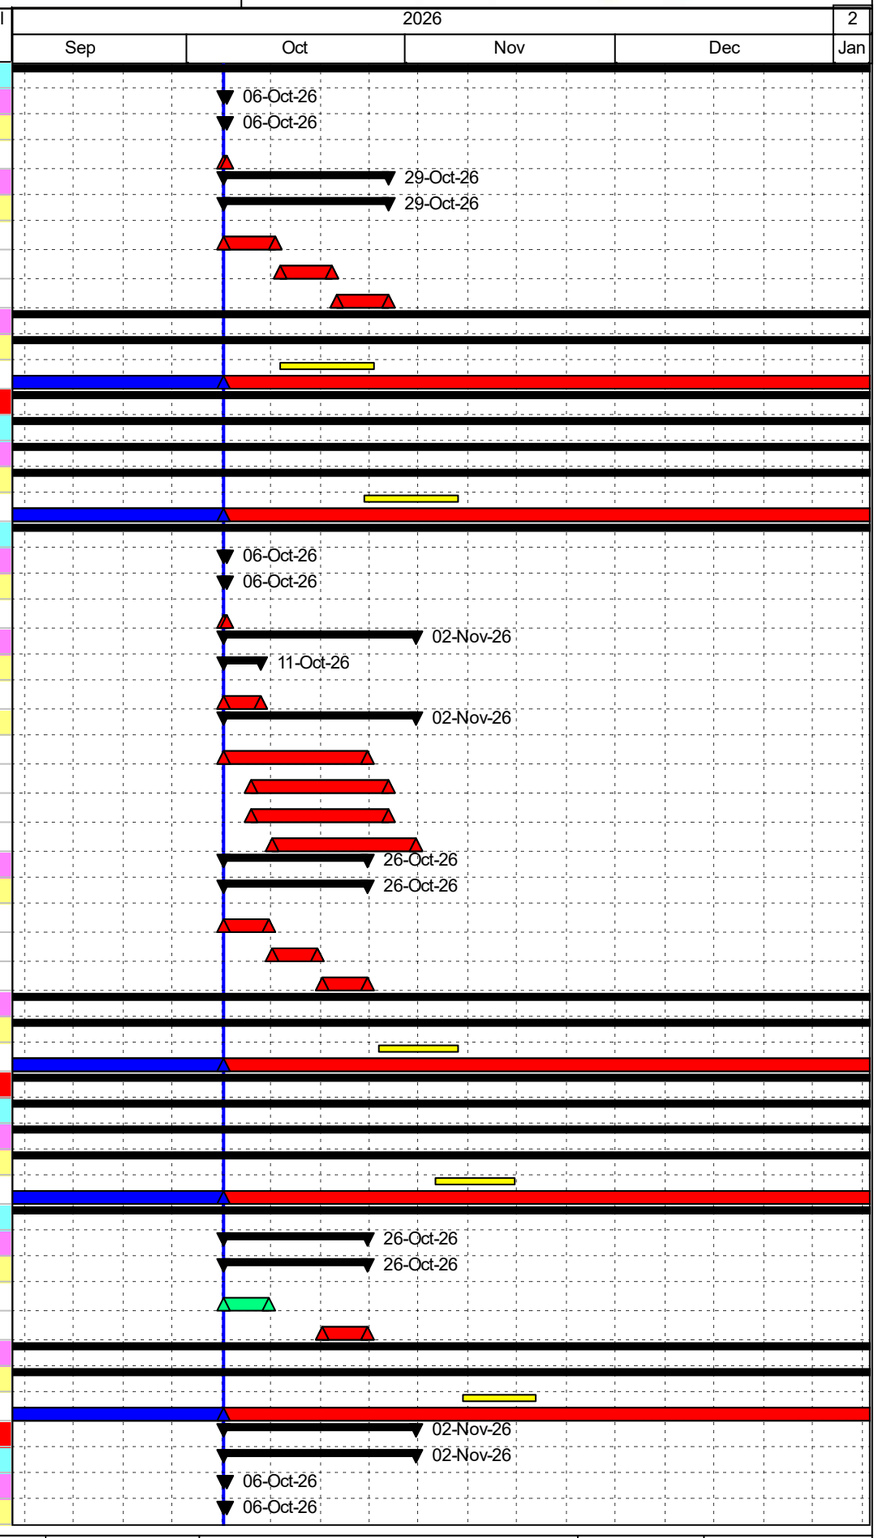


Primary Baseline | Actual Work | Summary
Remaining Work | Baseline Milestone
Critical Remaining Work | Milestone

Date	Revision	Checked	Approved
06-Oct-26	Third Industrial City		

Infrastructure Works of Area J -3rd Industrial City- Dammam-Phase 2 - Part 2 Update 06/10/2026
3Week Lookahead Schedule

Activity ID	Activity Name	Original Duration	Start	Finish	BL Project Start	BL Project Finish	Budgeted Total Cost
CO-R17.S14-SW-	Testing Works for Main Line Manholes of Sewage Network-[Road 17]-[SW-14]	1	06-Oct-26	06-Oct-26	21-May-25	21-May-25	1,517.62
Street Lighting Network		24	06-Oct-26	02-Nov-26	16-Apr-25	14-Dec-25	44,704.41
Lighting Poles Works		5	06-Oct-26	11-Oct-26	08-Dec-25	14-Dec-25	17,131.23
CO-R17.S14-SL-;	Testing Works for Lighting Poles of Street Lighting Network-[Road 17]-[SW-14]	5	06-Oct-26	11-Oct-26	08-Dec-25	14-Dec-25	17,131.23
Distrubution Panel Boards		24	06-Oct-26	02-Nov-26	16-Apr-25	13-May-25	27,573.18
CO-R17.S14-SL-	Foundation Excavation Works For Panel Boards of Street Lighting Network-[Road 17	18	06-Oct-26	26-Oct-26	16-Apr-25	06-May-25	0.00
CO-R17.S14-SL-	Installation Works for Panel Board Concrete Foundations of Street Lighting Network-	18	10-Oct-26	29-Oct-26	20-Apr-25	10-May-25	0.00
CO-R17.S14-SL-;	A wall of concrete blocks to install the KWH meter of Street Lighting Network-[Road 1	18	10-Oct-26	29-Oct-26	20-Apr-25	10-May-25	27,573.18
CO-R17.S14-SL-	Installation Works for Lighting Panel Boards of Street Lighting Network-[Road 17]-[S\	18	13-Oct-26	02-Nov-26	23-Apr-25	13-May-25	0.00
Potable Water Network		6	06-Oct-26	12-Oct-26	21-Apr-26	27-Apr-26	3,408.46
Fire Hydrant		6	06-Oct-26	12-Oct-26	21-Apr-26	27-Apr-26	3,408.46
CO-R17.S14-PW-	Excavation Works for Fire Hydrants of Potable Water Network-[Road 17]-[SW-14]	6	06-Oct-26	12-Oct-26	21-Apr-26	27-Apr-26	3,408.46
Telecom Network		21	06-Oct-26	29-Oct-26	09-Aug-26	01-Sep-26	6,258.47
Manholes Works		21	06-Oct-26	29-Oct-26	09-Aug-26	01-Sep-26	6,258.47
CO-R17.S14-TE-	Excavation Works for Manholes of Telecom Network-[Road 17]-[SW-14]	7	06-Oct-26	13-Oct-26	09-Aug-26	16-Aug-26	628.46
CO-R17.S14-TE-	Installation Works for Manholes of Telecom Network-[Road 17]-[SW-14]	7	14-Oct-26	21-Oct-26	17-Aug-26	24-Aug-26	5,001.55
CO-R17.S14-TE-	Backfilling Works for Manholes of Telecom Network-[Road 17]-[SW-14]	7	22-Oct-26	29-Oct-26	25-Aug-26	01-Sep-26	628.46
Road 18 Local 1 (479 LM)		24	06-Oct-26	02-Nov-26	19-Mar-25	27-Nov-25	51,658.33
SW_16		24	06-Oct-26	02-Nov-26	19-Mar-25	27-Nov-25	51,658.33
Street Lighting Network		24	06-Oct-26	02-Nov-26	19-Mar-25	27-Nov-25	36,509.63
Lighting Poles Works		19	06-Oct-26	27-Oct-26	08-Nov-25	27-Nov-25	20,573.15
CO-R18.S16-SL-;	Testing Works for Lighting Poles of Street Lighting Network-[Road 18]-[SW-16]	5	06-Oct-26	11-Oct-26	22-Nov-25	27-Nov-25	7,994.57
CO-R18.S16-SL-	Installation Works for Lighting Fixtures With Drop Wire of Street Lighting Network-[Rc	18	07-Oct-26	27-Oct-26	08-Nov-25	27-Nov-25	12,578.58
Distrubution Panel Boards		24	06-Oct-26	02-Nov-26	19-Mar-25	20-Apr-25	15,936.47
CO-R18.S16-SL-	Foundation Excavation Works For Panel Boards of Street Lighting Network-[Road 18	18	06-Oct-26	26-Oct-26	19-Mar-25	13-Apr-25	0.00
CO-R18.S16-SL-	Installation Works for Panel Board Concrete Foundations of Street Lighting Network-	18	10-Oct-26	29-Oct-26	23-Mar-25	16-Apr-25	0.00
CO-R18.S16-SL-;	A wall of concrete blocks to install the KWH meter of Street Lighting Network-[Road 1	18	10-Oct-26	29-Oct-26	23-Mar-25	16-Apr-25	15,936.47
CO-R18.S16-SL-	Installation Works for Lighting Panel Boards of Street Lighting Network-[Road 18]-[S\	18	13-Oct-26	02-Nov-26	26-Mar-25	20-Apr-25	0.00
Potable Water Network		18	06-Oct-26	26-Oct-26	23-Aug-25	11-Sep-25	15,148.70
Fire Hydrant		18	06-Oct-26	26-Oct-26	23-Aug-25	11-Sep-25	15,148.70
CO-R18.S16-PW-	Excavation Works for Fire Hydrants of Potable Water Network-[Road 18]-[SW-16]	6	06-Oct-26	12-Oct-26	23-Aug-25	28-Aug-25	2,272.30
CO-R18.S16-PW-	Installation Works for Fire Hydrant of Potable Water Network-[Road 18]-[SW-16]	6	13-Oct-26	19-Oct-26	30-Aug-25	04-Sep-25	9,846.66
CO-R18.S16-PW-	Trench Backfilling and Compaction Works for Fire Hydrants of Potable Water Networl	6	20-Oct-26	26-Oct-26	06-Sep-25	11-Sep-25	3,029.74
Finishes for Infrastructure Networks		65	01-Jun-26 A	28-Jun-27	15-Jul-26	03-Oct-26	1,796,955.97
Phase 2 Block "J"		65	01-Jun-26 A	28-Jun-27	15-Jul-26	03-Oct-26	1,796,955.97
Road 09 Local 2 (2278 LM)		40	01-Jun-26 A	15-Jun-27	15-Jul-26	02-Sep-26	967,473.22
Sewage Network		12	01-Jun-26 A	08-May-27	19-Jul-26	01-Aug-26	208,794.34
Testing and Finishes		12	01-Jun-26 A	08-May-27	19-Jul-26	01-Aug-26	208,794.34
CO-R09-SW-TF-1	Final Testing For Main Line of Sewage Network-[Road 09]	12	01-Jun-26 A	08-May-27	19-Jul-26	01-Aug-26	208,794.34
Storm Drainage Network		33	17-Jun-26 A	15-Jun-27	15-Jul-26	02-Sep-26	758,678.88
Testing and Finishes		33	17-Jun-26 A	15-Jun-27	15-Jul-26	02-Sep-26	758,678.88
CO-R09-SD-TF-1(	Testing Work for Pipes of Storm Drainage Network-[Road 09]	12	17-Jun-26 A	09-May-27	19-Jul-26	01-Aug-26	101,957.42
CO-R09-SD-TF-1'	Install Catch Basin Cover Works for External Finishes of Storm Drainage Network-[R	16	20-Jun-26 A	09-May-27	15-Jul-26	02-Aug-26	27,719.40
CO-R09-SD-TF-1:	Main Manhole Internal Finishes (Benching + Insulation) for Storm Drainage Network	16	21-Jun-26 A	15-Jun-27	16-Aug-26	02-Sep-26	601,282.66
CO-R09-SD-TF-1:	Catch Basin Internal Finishes (Benching + Insulation) for Storm Drainage Network-[F	16	22-Jun-26 A	15-Jun-27	16-Aug-26	02-Sep-26	27,719.40
Road 10 Local 2 (2352 LM)		35	17-Jun-26 A	09-Jun-27	04-Aug-26	13-Sep-26	558,232.55
Storm Drainage Network		35	17-Jun-26 A	09-Jun-27	04-Aug-26	13-Sep-26	558,232.55
Testing and Finishes		35	17-Jun-26 A	09-Jun-27	04-Aug-26	13-Sep-26	558,232.55
CO-R10-SD-TF-1'	Install Catch Basin Cover Works for External Finishes of Storm Drainage Network-[R	16	17-Jun-26 A	10-May-27	04-Aug-26	22-Aug-26	27,795.73
CO-R10-SD-TF-1:	Main Manhole Internal Finishes (Benching + Insulation) for Storm Drainage Network	12	18-Jun-26 A	05-Jun-27	26-Aug-26	08-Sep-26	502,641.74
CO-R10-SD-TF-1:	Catch Basin Internal Finishes (Benching + Insulation) for Storm Drainage Network-[F	16	22-Jun-26 A	09-Jun-27	26-Aug-26	13-Sep-26	27,795.08
Road 11 Local 1 (670 LM)		28	22-Jun-26 A	28-Jun-27	23-Aug-26	03-Oct-26	271,250.20
Storm Drainage Network		28	22-Jun-26 A	28-Jun-27	23-Aug-26	03-Oct-26	271,250.20

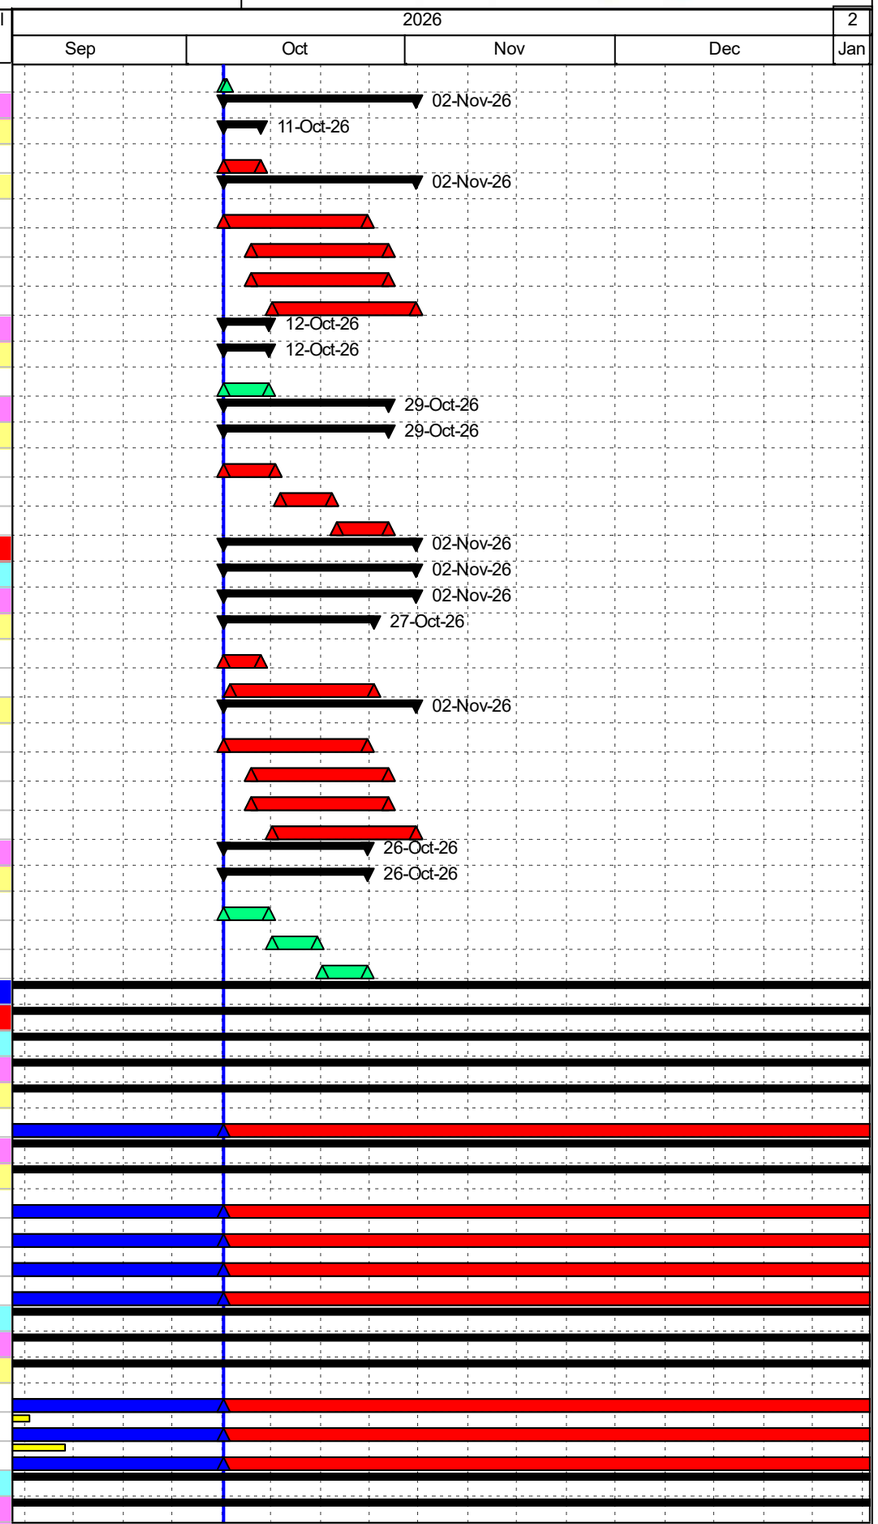


Primary Baseline | Actual Work | Summary
Remaining Work | Baseline Milestone
Critical Remaining Work | Milestone

Date	Revision	Checked	Approved
06-Oct-26	Third Industrial City		

Infrastructure Works of Area J -3rd Industrial City-
Dammam-Phase 2 - Part 2 Update 06/10/2026
3Week Lookahead Schedule

Activity ID	Activity Name	Original Duration	Start	Finish	BL Project Start	BL Project Finish	Budgeted Total Cost
Testing and Finishes		28	22-Jun-26 A	28-Jun-27	23-Aug-26	03-Oct-26	271,250.20
CO-R11-SD-TF-1	Catch Basin Internal Finishes (Benching + Insulation) for Storm Drainage Network-[F	16	22-Jun-26 A	28-Jun-27	14-Sep-26	03-Oct-26	8,111.50
CO-R11-SD-TF-1	Main Manhole Internal Finishes (Benching + Insulation) for Storm Drainage Network	12	23-Jun-26 A	19-Jun-27	09-Sep-26	22-Sep-26	255,027.20
CO-R11-SD-TF-1	Install Catch Basin Cover Works for External Finishes of Storm Drainage Network-[R	12	27-Jun-26 A	30-May-27	23-Aug-26	05-Sep-26	8,111.50
Independent Works		53	16-Sep-26 A	26-Dec-26	15-Feb-26	09-May-26	72,713.76
Sewage Pump Stations		30	16-Sep-26 A	26-Dec-26	05-Apr-26	09-May-26	66,973.20
Sewage Pump Station (PS 06)		30	16-Sep-26 A	26-Dec-26	05-Apr-26	09-May-26	66,973.20
Pump Station Main Building		30	16-Sep-26 A	26-Dec-26	05-Apr-26	09-May-26	66,973.20
CO-SW-PS7-MB-11	Concrete Works of Superstrucure	30	16-Sep-26 A	26-Dec-26	05-Apr-26	09-May-26	66,973.20
Storm Drainage Ponds		21	06-Oct-26	29-Oct-26	15-Feb-26	10-Mar-26	5,740.56
Storm Drainage Pond (PO-J1)		21	06-Oct-26	29-Oct-26	15-Feb-26	10-Mar-26	5,740.56
CO-SD-PO-K1-110-P	Finished Grouted Riprap - PART 1	21	06-Oct-26	29-Oct-26	15-Feb-26	10-Mar-26	5,740.56
Testing and Comissioning		118	01-Jun-26 A	31-Oct-27	07-Nov-26	03-Jan-27	11,075,668.52
Infrastructure Networks		118	01-Jun-26 A	31-Oct-27	07-Nov-26	03-Jan-27	11,075,668.52
Irrigation Network		12	05-Jun-26 A	10-Aug-27	12-Nov-26	25-Nov-26	624,273.76
T/C-IR	Testing and Commissioning of Irrigation Network	12	05-Jun-26 A	10-Aug-27	12-Nov-26	25-Nov-26	624,273.76
Potable Water Network		12	01-Jul-26 A	28-Sep-27	03-Dec-26	16-Dec-26	1,022,094.20
T/C-PW	Testing and Commissioning of Potable Water Network	12	01-Jul-26 A	28-Sep-27	03-Dec-26	16-Dec-26	1,022,094.20
Sewage Network		12	01-Jun-26 A	10-Oct-27	19-Dec-26	31-Dec-26	2,308,897.10
T/C-SW	Testing and Commissioning of Sewage Network	12	01-Jun-26 A	10-Oct-27	19-Dec-26	31-Dec-26	2,308,897.10
Storm Drainage Network		10	10-Jun-26 A	12-Sep-27	21-Dec-26	31-Dec-26	2,866,651.20
T/C-SD	Testing and Commissioning of Storm Drainage Network	10	10-Jun-26 A	12-Sep-27	21-Dec-26	31-Dec-26	2,866,651.20
Street Lighting Network		18	05-Sep-26 A	24-Oct-27	07-Nov-26	26-Nov-26	462,378.20
T/C-SL	Testing and Commissioning of Street Lighting Network	18	05-Sep-26 A	24-Oct-27	07-Nov-26	26-Nov-26	462,378.20
Telecom Network		10	05-Sep-26 A	20-Sep-27	10-Nov-26	21-Nov-26	181,657.10
T/C-TE	Testing and Commissioning of Telecom Network	10	05-Sep-26 A	20-Sep-27	10-Nov-26	21-Nov-26	181,657.10
Medium Voltage Network		10	05-Sep-26 A	03-Oct-27	22-Nov-26	02-Dec-26	478,905.06
T/C-MV	Testing and Commissioning of Medium Voltage Network	10	05-Sep-26 A	03-Oct-27	22-Nov-26	02-Dec-26	478,905.06
Road Works		5	16-Aug-26 A	31-Oct-27	29-Dec-26	03-Jan-27	3,130,811.90
T/C-RD	Testing and Commissioning of Road Works	5	16-Aug-26 A	31-Oct-27	29-Dec-26	03-Jan-27	3,130,811.90

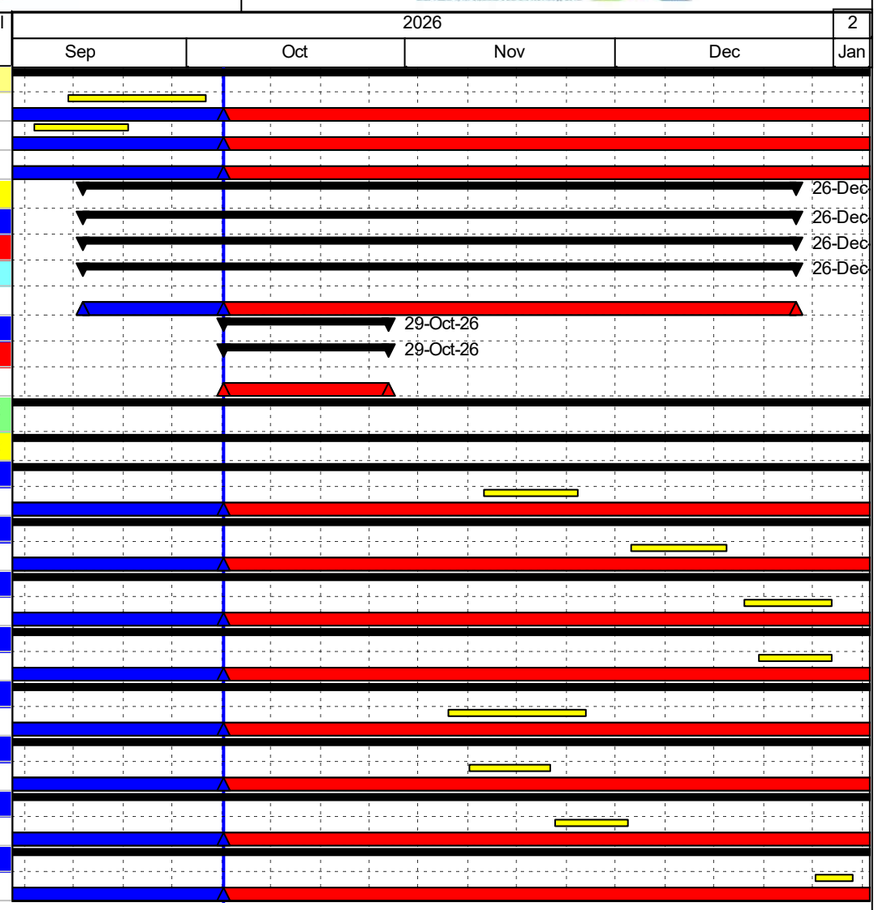

Primary Baseline
Remaining Work
Critical Remaining Work
Actual Work
Baseline Milestone
Milestone
Summary

Date	Revision	Checked	Approved
06-Oct-26	Third Industrial City		
