
Infrastructure Works of Area J -3rd Industrial City-Dammam-Phase 2 - Part 2 Update 06/10/2026

WBS Summary Schedule

Activity ID	Activity Name	Original Duration	BL Project Start	BL Project Finish	Start	Finish	Performance % Complete
Infrastructure Works of Area J -3rd Industrial City-Dammam-Pha		856	12-Jan-25	11-Jan-27	12-Jan-25 A	08-Nov-27	73.85%
Key Milestones		856	12-Jan-25	11-Jan-27	12-Jan-25 A	08-Nov-27	0%
Preliminaries and Mobilization Works		48	12-Jan-25	09-Mar-25	12-Jan-25 A	12-Mar-25 A	0%
Engineering Works		165	12-Jan-25	16-Feb-25	12-Jan-25 A	02-Jun-25 A	100%
Procurement Cycle		743	05-Feb-25	05-Oct-26	11-Feb-25 A	22-Jul-27	86.97%
Construction Works		820	09-Feb-25	28-Dec-26	11-Feb-25 A	25-Oct-27	71.4%
Testing and Comissioning		130	25-Aug-26	03-Jan-27	01-Jun-26 A	31-Oct-27	61.66%
Handing over and close out		100	17-Oct-26	11-Jan-27	14-Jul-27	08-Nov-27	0%

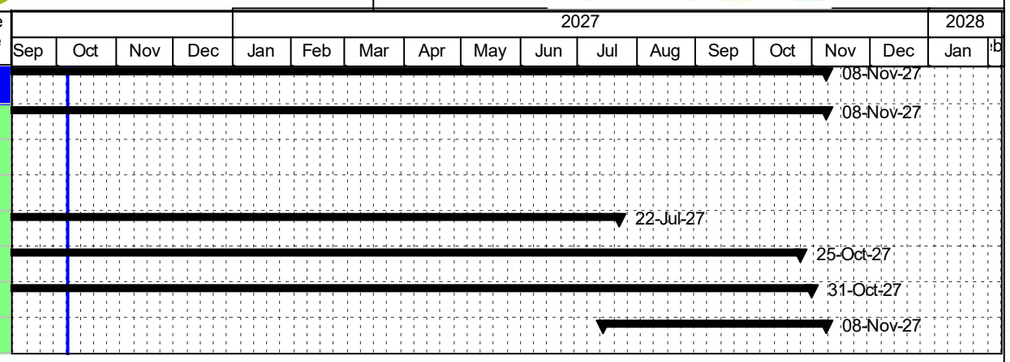

Primary Baseline
Remaining Work
Critical Remaining Work
Actual Work
Baseline Milestone
Milestone
Summary

Date	Revision	Checked	Approved
06-Oct-26	Third Industrial City		
