Development of Phase One – Part Two, Third Industrial City in Dammam

مشروع تطوير المرحلة الأولى الجزء الثاني بالمدينة الصناعية الثالثة بالدمام

CLIENT	CONTRACTOR	CONSULTANT	MODON PM	SITE HANDOVER	CONTRACT COMPLETION
MODON	Mofarreh Alharbi and Partners	EGIS	Ihab Mohammed Attia	19-May-2025	18-May-2027

Scope: arterial and local roads, potable water, sewage, storm drainage, irrigation, street lighting and telecom networks, sewage pump stations and storm drainage ponds for Phase 1, Part 2 of the 3rd Industrial City in Dammam.

Status at a glance

Progress is measured as physical % complete, weighted by budgeted man-hours. At the 03-Nov-2026 data date the project is 77.6% complete against 96.6% planned, 19.0% behind plan. It gained 0.22% this week against 0.12% planned, slightly above the weekly plan but far below the rate needed to finish on time.

PHYSICAL % COMPLETE
77.6% / 96.6% plan
▼ SPI 0.80 –19.0%

PROGRESS THIS WEEK
+0.22% / +0.12% plan
▲ 0.10% above the weekly plan

CONTRACT TIME ELAPSED
73.2% · day 534 of 730
▼ P6 finish 27-Oct-2027

INVOICED TO DATE (GROSS)
15.9% · 37.3M SAR
12 progress invoices, last period ends 15-Jul-2026

The P6 update now finishes the project 162 days late.

The P6 update uploaded this week (data date 31-Oct-2026) schedules project finish on 27-Oct-2027, 162 days after the contract completion date of 18-May-2027, with –162 days of float; the weekly report still forecasts 18-May-2027. To finish on the contract date, the remaining 22.4% needs about 0.80% a week over the 28 whole weeks left; this week achieved 0.22%. The weakest areas remain the Zone 3 networks (67.0% against 98.2% planned), the sewage networks in Zones 1 and 3, and the road crossings.

Site photos this week

Six photo sheets uploaded with this week's report, dated 25 to 28 October 2026 by the contractor. Work centred on testing the water lines, valves and fire hydrants, a mandrel test of the telecom ducts, lift station pipework and adjusting storm water grating levels. Select a photo to view it larger, then use the arrows to move between photos.



Hydrostatic pressure test

Pressure test of the water lines. Zone 3, Road 25, 25-Oct-2026.



Valve on the potable water line

Joint welding and valve installation to complete the hydrotest. Zone 2, Road 13, 27-Oct-2026.



Fire hydrant installation

Zone 2, Road 9, 28-Oct-2026.



Telecom duct mandrel test

Checking the telecom ducts for blockages and deformation. Zones 1 and 2, 26-Oct-2026.



Lift station pipework

Removing a flange adaptor and cutting ductile iron pipe to set the riser levels. Zone 1, Lift Station 2, 28-Oct-2026.




Storm water grating levels

Breaking the concrete around catch basin gratings to adjust their levels. Zone 2, Road 11, 25-Oct-2026.

Progress S-curve

Cumulative physical progress (man-hour weighted), monthly. Source: Physical-Chart Data sheet; October and November actuals from the weekly reports.

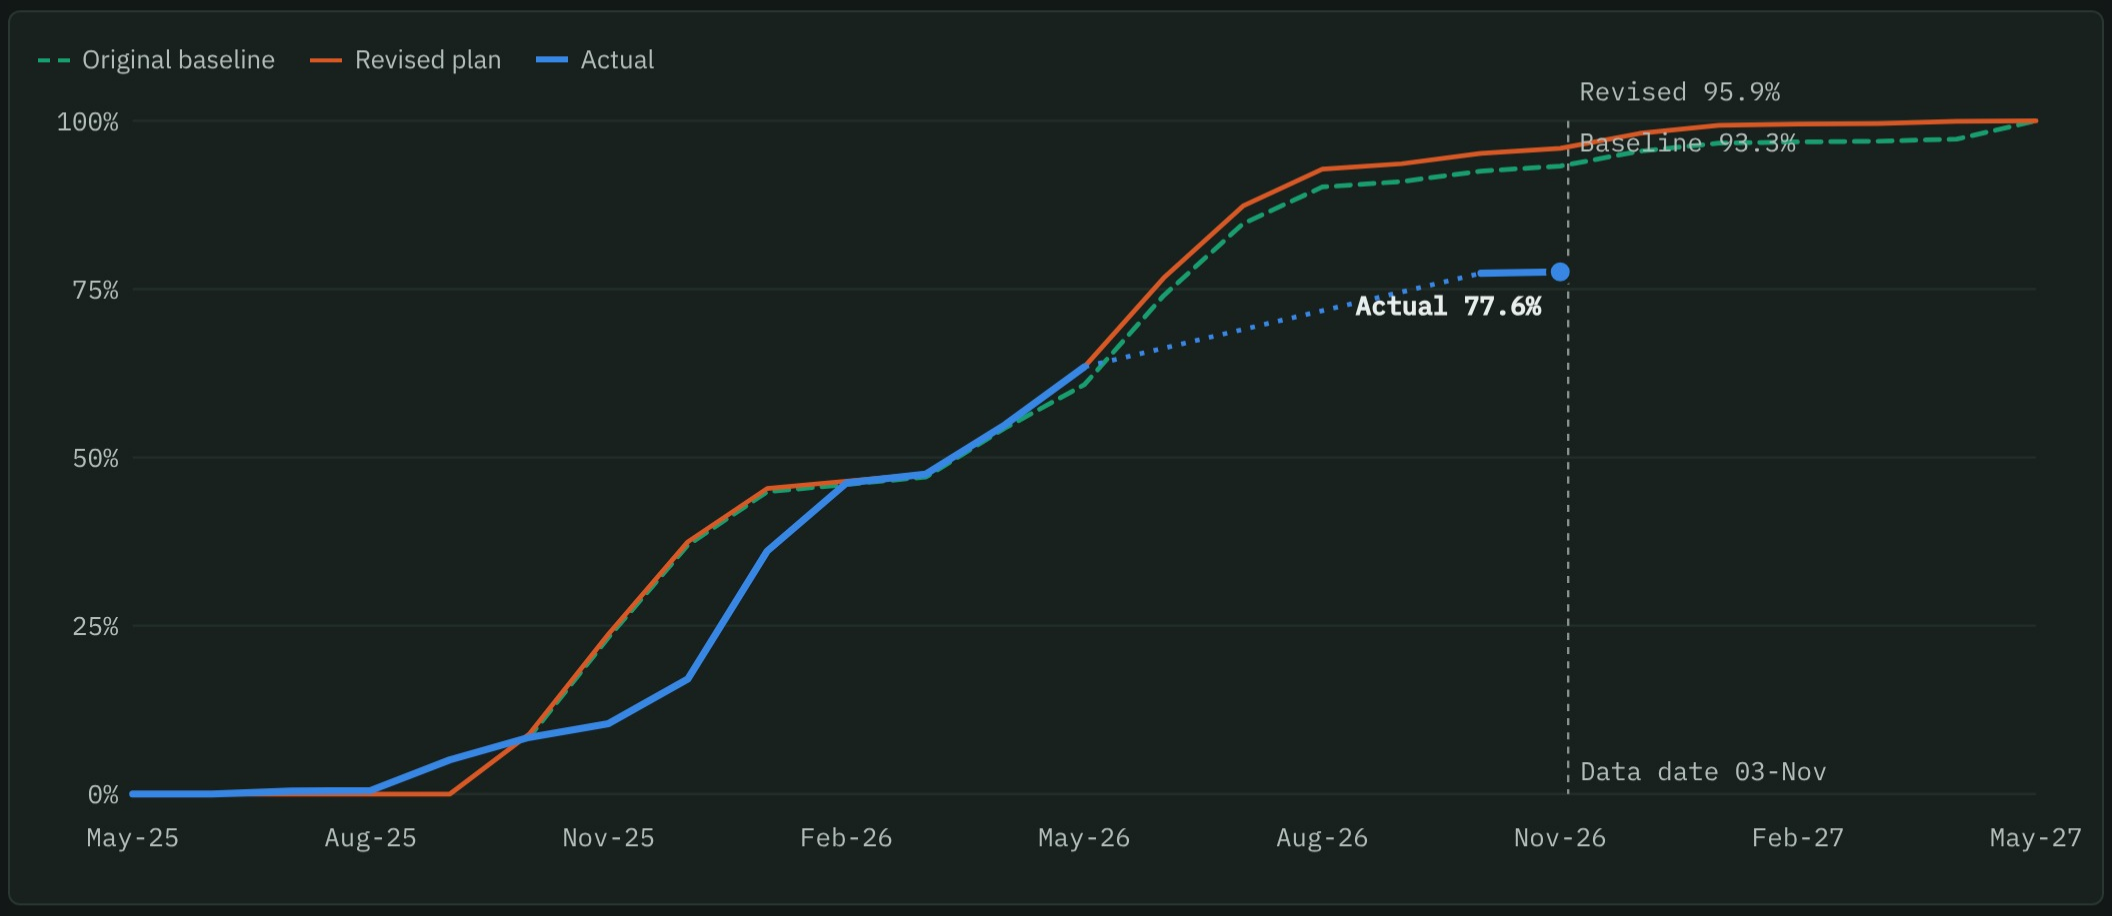

WEEK ENDING	PLANNED %	ACTUAL %	VARIANCE	GAINED THIS WEEK	SPI
27-Oct-2026	96.5	77.4	−19.1%	+0.07%	0.80
03-Nov-2026	**96.6**	**77.6**	**−19.0%**	**+0.22%**	**0.80**

Two weekly reports have been uploaded (27-Oct and 03-Nov). The chart sheet has reliable monthly actuals only up to May 2026; the dotted line joins May to the weekly figures for October (77.4%) and November (77.6%). The weekly report's planned 96.6% is higher than both the baseline (93.3%) and the revised plan (95.9%) for November.

Progress by phase


Physical progress to date by zone and network, weighted by budgeted man-hours. Engineering and procurement carry no man-hours, so they have no physical measure.

PHASE	WEIGHT	PLANNED	ACTUAL	VARIANCE	SPI	STATUS
Zone 1	42.1%	**96.0%**	**82.0%**	**-14.0%**	**0.85**	▼ Behind
Sewage network	7.0%	92.2%	59.5%	-32.7%	0.65	▼ Late
Storm drainage network	4.4%	100.0%	81.5%	-18.5%	0.81	▼ Late
Potable water network	3.1%	100.0%	94.9%	-5.1%	0.95	▼ Behind
Irrigation network	2.1%	100.0%	96.8%	-3.2%	0.97	▲ On track
Storm water collection ponds	24.3%	96.3%	89.9%	-6.4%	0.93	▼ Behind
Road crossings	1.3%	80.7%	0.0%	-80.7%	0.00	▼ Not started
Zone 2	20.0%	**99.8%**	**83.7%**	**-16.1%**	**0.84**	▼ Late
Sewage network	3.9%	100.0%	81.4%	-18.6%	0.81	▼ Late
Storm drainage network	4.4%	100.0%	77.6%	-22.4%	0.78	▼ Late
Potable water network	0.8%	100.0%	88.1%	-12.0%	0.88	▼ Behind
Irrigation network	2.7%	100.0%	96.3%	-3.7%	0.96	▲ On track
Storm water collection ponds	6.9%	99.5%	98.9%	-0.6%	0.99	▲ On track
Road crossings	1.3%	100.0%	0.0%	-100.0%	0.00	▼ Not started
Zone 3	31.5%	**98.2%**	**67.0%**	**-31.2%**	**0.68**	▼ Late
Sewage network	7.6%	93.0%	49.6%	-43.4%	0.53	▼ Late
Storm drainage network	5.3%	100.0%	71.3%	-28.7%	0.71	▼ Late
Potable water network	6.1%	100.0%	45.2%	-54.8%	0.45	▼ Late
Irrigation network	0.8%	100.0%	90.4%	-9.6%	0.90	▼ Behind
Storm water collection ponds	11.0%	99.7%	89.3%	-10.4%	0.90	▼ Behind
Road crossings	0.6%	100.0%	31.8%	-68.2%	0.32	▼ Late
General	6.4%	**62.3%**	**58.0%**	**-4.3%**	**0.93**	▼ Behind
Local roads *	0.4%	6.9%	33.1%	+26.3%	4.83	▲ Ahead
Arterial roads *	0.4%	100.0%	17.4%	-82.6%	0.17	▼ Late
Telecom *	3.8%	82.1%	93.0%	+10.9%	1.13	▲ Ahead
Landscape	1.9%	26.3%	0.0%	-26.3%	0.00	▼ Not started
Total	100%	**96.6%**	**77.6%**	**-19.0%**	**0.80**	▼ Late

Planned and actual from the Weekly Progress Report sheet. * Zone 3, local roads, arterial roads and telecom use the cumulative actual man-hours of the P6 export in the Progress sheet, because the summary rows for them are inconsistent (see Data notes). The P6 update (data date 31-Oct-2026) has 1,255 activities: 488 completed, 416 in progress and 351 not started.

Scope of work: quantities

Quantities in the Alharbi (MG) scope, from the 03-Nov-2026 weekly presentation: network pipes from the network quantities slide, and manholes, valves, hydrants and lighting from the progress scope slide. "This week" is the change since the 27-Oct-2026 presentation.

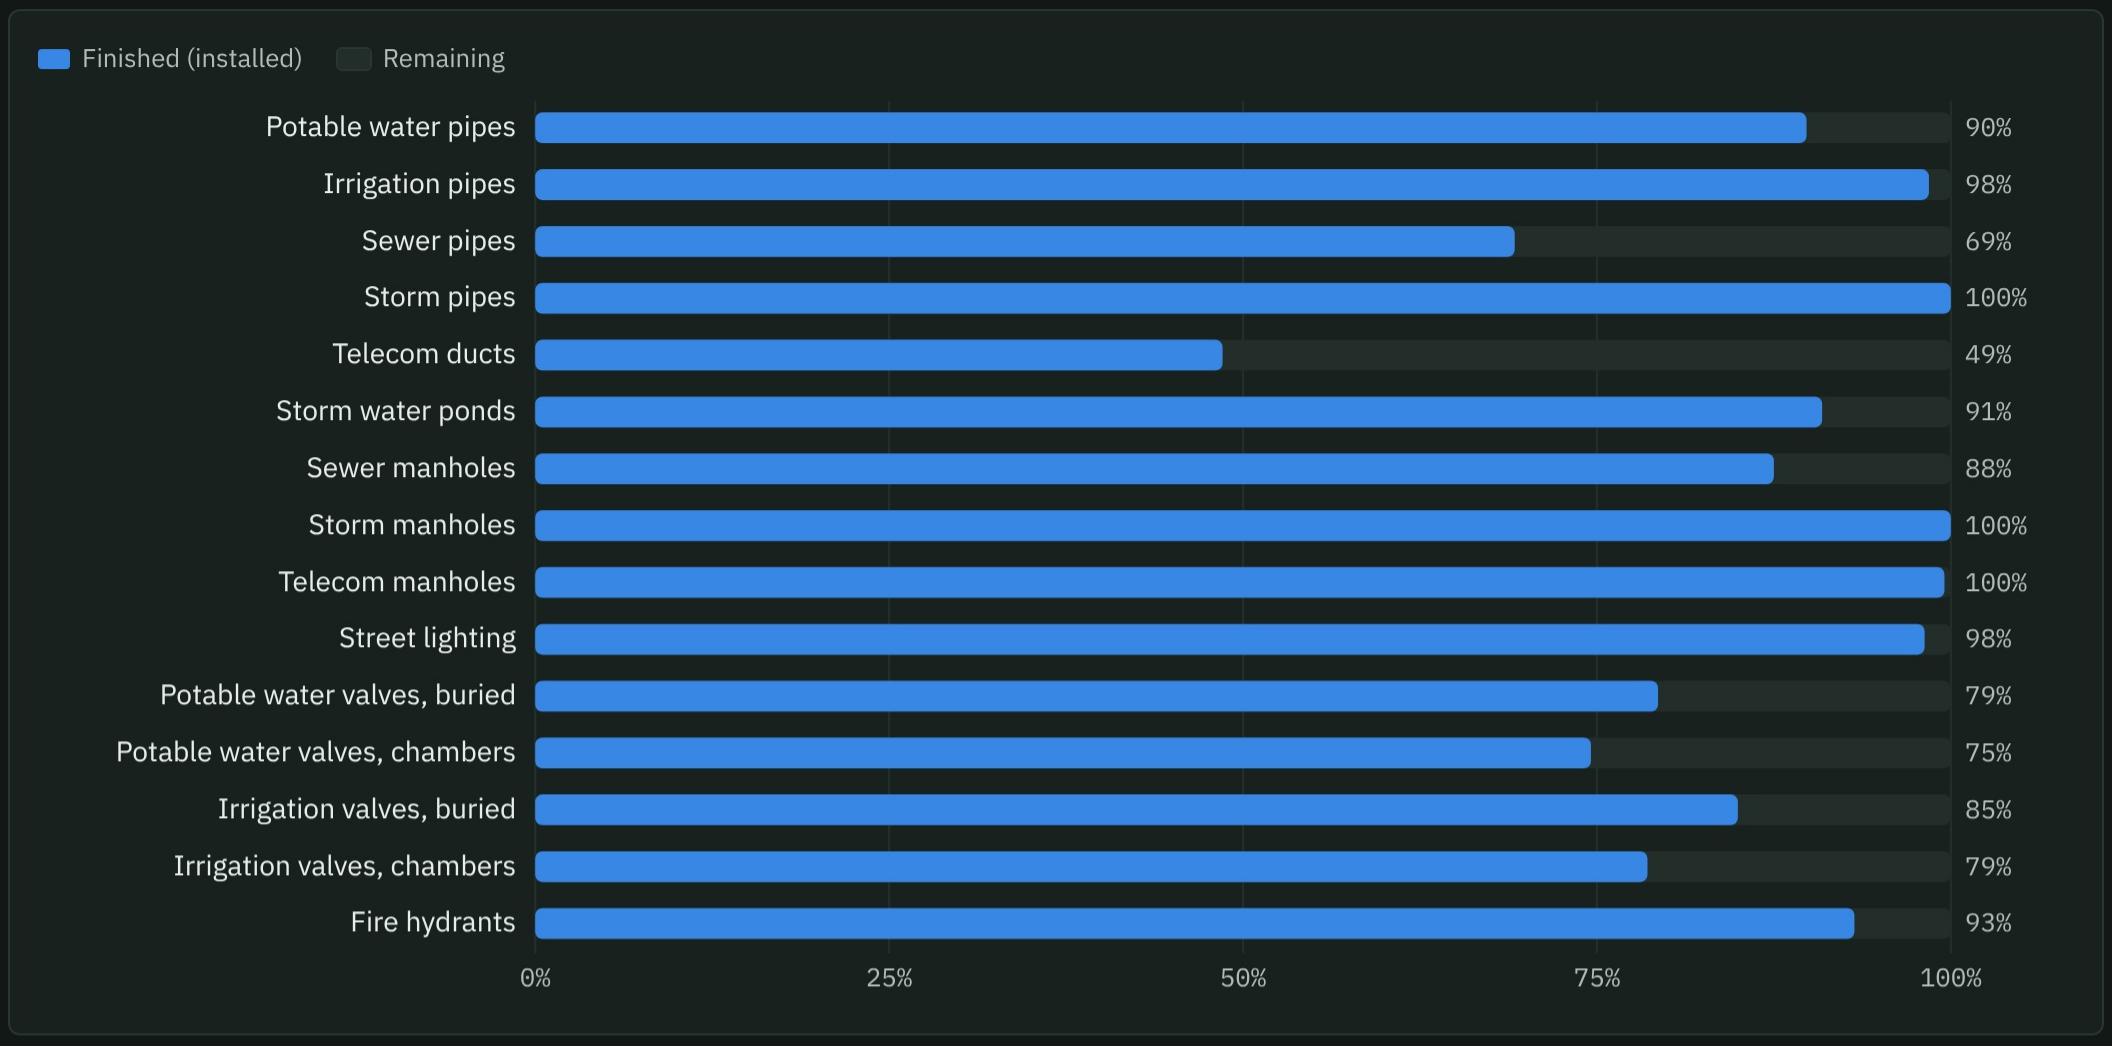

SCOPE ITEM	ZONE	UNIT	TOTAL	FINISHED	THIS WEEK	REMAINING	% FINISHED	BACKFILLED
Potable water pipes	All zones	m	2,992	2,687	0	305	89.8%	–
Irrigation pipes	All zones	m	4,911	4,835	0	76	98.5%	–
Sewer pipes	All zones	m	396	274	0	122	69.2%	–
Storm pipes	All zones	m	42,616	42,616	0	0	100.0%	–
Telecom ducts	All zones	m	64,321	31,233	0	33,088	48.6%	–
Storm water ponds	All zones	nos	11	10	0	1	90.9%	–
Sewer manholes	All zones	nos	104	91	+1	13	87.5%	–
Storm manholes	All zones	nos	13	13	0	0	100.0%	–
Telecom manholes	All zones	nos	444	442	0	2	99.5%	–
Street lighting	All zones	unit not stated	54	53	0	1	98.1%	–
Potable water valves, buried	All zones	nos	440	349	0	91	79.3%	–
Potable water valves, chambers	All zones	nos	59	44	0	15	74.6%	–
Irrigation valves, buried	All zones	nos	884	751	+3	133	85.0%	–
Irrigation valves, chambers	All zones	nos	70	55	0	15	78.6%	–
Fire hydrants	All zones	nos	279	260	+9	19	93.2%	–

Telecom and sewage are the largest open quantities

No network pipe length was added this week: telecom ducts remain 49% installed (31,233 of 64,321 m) and sewer pipes 69% (274 of 396 m). Telecom handed to the consultant rose from 6,705 m to 11,175 m; 2,184 m of potable water and 2,998 m of irrigation have also been handed over, and no sewer or storm lengths yet.

Previous contractor's networks

Alharbi has re-tested 74,073 m of water, 77,912 m of irrigation and 38,914 m of sewer from the previous contractor's scope, but only 8,588 m, 3,442 m and 9,343 m have been handed to the consultant. 31,676 m of storm network and 5,516 m of telecom remain to be tested.

Milestones

The weekly report keeps every forecast on the baseline date, while the P6 update shows the interim network milestones and completion late. Both are shown so the difference can be resolved with the contractor.

MILESTONE	BASELINE	WEEKLY REPORT FORECAST	P6 UPDATE FORECAST	P6 FLOAT (DAYS)	STATUS
Site handover	19-May-2025	19-May-2025	19-May-2025 (actual)	–	✓ Done
Site preparations	18-Jun-2025	18-Jun-2025	17-Jun-2025 (actual)	–	✓ Done
Report, work plan and schedule submitted	18-Jul-2025	18-Jul-2025	31-Oct-2026	+200	? Open in P6
Drawings and specifications approved	18-Jul-2025	18-Jul-2025	05-Nov-2026	−189	? Open in P6
Water networks and tanks complete	18-Jan-2026	18-Jan-2026	20-Jan-2027	−20	▼ Late
Rainwater drainage works complete	18-Jan-2026	18-Jan-2026	31-Dec-2026	−158	▼ Late
Completion of all project services	18-May-2027	18-May-2027	19-Oct-2027	−154	▼ Late
Final handover	18-May-2027	18-May-2027	27-Oct-2027	−162	▼ Late

The P6 update and the weekly report are 162 days apart on completion.

This week's P6 update (1,255 activities, data date 31-Oct-2026) and the P6 export in the weekly report workbook both finish the project on 27-Oct-2027. Last week's upload was a different, 136-activity revised schedule finishing on 12-Jun-2027, so the two weeks' P6 dates cannot be compared directly. The weekly report forecasts 18-May-2027 with no delay. The water and rainwater milestones of 18-Jan-2026 are now forecast for 20-Jan-2027 and 31-Dec-2026.

Procurement of key materials

Share of total quantity delivered to site for the long-lead items. Source: weekly presentation 03-Nov-2026, long-lead items slide.



Pumps: 2 of 15 delivered


Grundfos pump accessories are being installed at the stations, but only 2 pumps have arrived because of global shipping problems (last week's presentation said 3). The water station control panel (IGEC, 1 set) and sewage station panels (WAMCO, 4 sets) are not expected in full until January 2027; the control system target is now 28-Jan-2027.

Generators and surge vessels

The two generators (Kohler – Abunayyan) are in the Kingdom and wait for the factory and site acceptance tests before delivery to site. Surge vessel deliveries (7) are now expected to start around 05-Nov-2026, moved from 15-Oct-2026. The VEGA supplier has given no delivery date. The water pump maintenance order (SPP) is waiting for parts.

Manpower

Monthly head count on site (staff and labour), planned vs actual. Source: Manpower sheet.

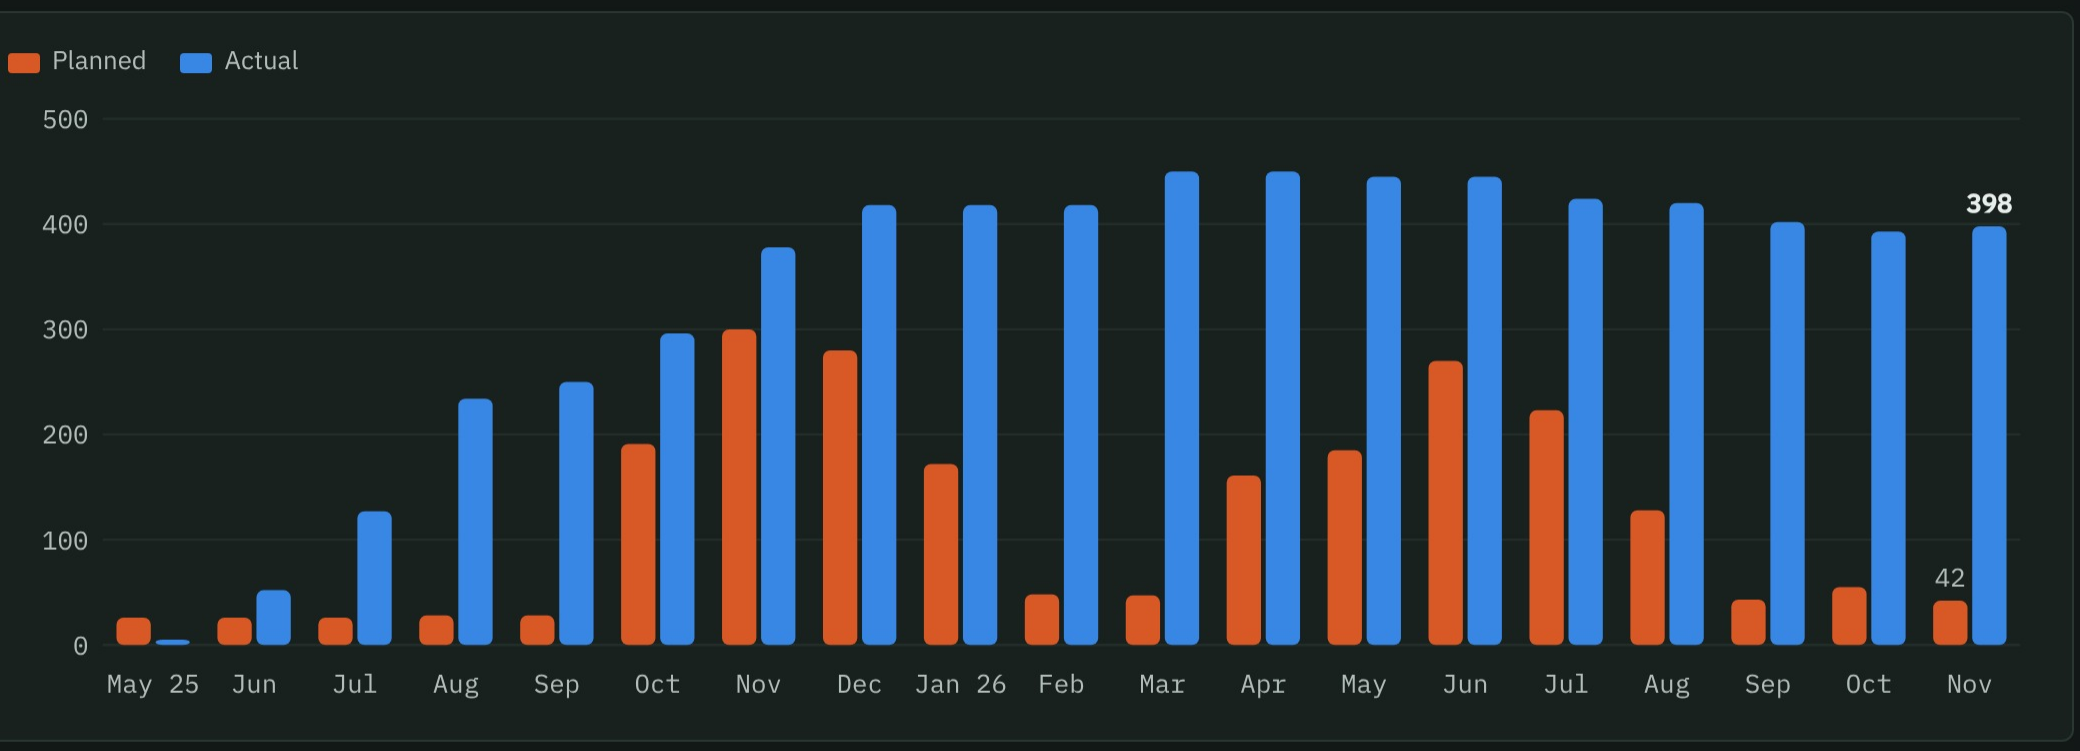

November head count is 398 (66 staff and 332 labour) against 42 planned. The plan comes from the resource-loaded P6 schedule and is far below the numbers actually on site, so it is not a useful benchmark. Labour has fallen from 397 in March–April to 332; the issue log names low manpower and productivity as a cause of delay.

Cost and invoicing

Contract value

Original contract value (weekly report)	233,776,077
Contract value (presentation, excl. VAT)	233,575,734
Current project value after scope saving	164,170,171
Current saving	69,405,562
Change orders	0

All values in SAR. The two contract values differ by 200,343 SAR. The presentation records a scope reduction to 164.2M SAR; no change order is registered for it.

Invoices

Progress invoices submitted / approved	12 / 12
Gross value submitted	37,272,238
Advance payment (10%)	23,377,608
Retention (10%)	6,064,985
Invoices paid	4 · 15,540,346
Total disbursed to invoice 14 (presentation)	65,141,130
Executed but not yet paid (presentation)	13,310,176

The weekly report counts invoices to the period ending 15-Jul-2026; the presentation counts disbursements to invoice 14 (September 2026), 27.9% of the contract value. Invoicing stays well below the 77.6% physical progress.

Health, safety and quality

Safety Score 0.84

Safe man-hours (cumulative)	1,573,676
Man-hours this week	25,680
Lost-time injuries	0
Fatalities	0
First-aid cases	13
Near misses	1
Property damage	8
Inductions / toolbox talks	1,342 / 111

HSE inspection week: 28 Oct – 03 Nov 2026. The issue log rates weak HSE procedures as critical.

Quality Score 0.91

FIRs issued / closed / open	6,367 / 6,299 / 68
NCRs issued / closed	53 / 52
Site instructions issued / open	90 / 3
MIRs issued / open	113 / 0
Shop drawings submitted (of 1,698)	1,687
Shop drawings approved A / B	306 / 1,368
Material submittals approved A / B	7 / 101

Quality inspection day: 03-Nov-2026.

Open issues and risks

ISSUE	OWNER	DETAIL
Pond 4	Contractor	MODON approved the proposal. Work starts after the sewer network at the junction of Road 25 and Road 9; new target 14-Nov-2026 (was 30-Sep-2026).
Road 25 crossings	Contractor	Asphalt cutting on Road 25 for the buried networks: the junction with Road 2 is done and the junction with Road 9 is in progress. Phases 1 and 2 follow once the city administration approves a traffic diversion; target 15-Nov-2026.
Permits on Roads 25 and 1	Consultant / Owner	Permit issue is suspended on Roads 25 and 1 and works there are stopped. Permits were requested and submitted; awaiting approval.
Block F and Road 9	Consultant / Owner	Works in Block F stopped from 06-Oct-2026 until power is connected to the Chinese factory. Work on Road 9 in area F is banned (partial stop) despite an approved permit.
Sewer manholes and box culvert	Consultant / Owner	22 sewer manholes have connections that clash with the storm water box culvert, blocking pipe connections. The contractor's proposal is to be reviewed by the consultant and sent to the owner; target 05-Nov-2026.
Pump station equipment	Contractor	Generators, surge vessels and pumps are paid and being manufactured; 2 sewage pumps and the fire pumps have been delivered (target 30-Nov-2026). Water pump maintenance has a purchase order; target 15-Nov-2026.
Third-party interfaces	Consultant / Owner	Slab settlement caused by Watco and Al-Issa works: several meetings held, no response from Al-Issa. The Al-Issa office gate conflicts with a lighting pole foundation.
Network testing	Contractor	Testing is needed so complete networks can be handed over. The test plan has been submitted and testing is under way.
Manpower and productivity	Contractor	Low manpower and equipment and low productivity of the contractor's own crews (MODON issue log, high priority). Excavation is done by hand because there are no records of the existing services.

Open risks in the MODON register: change in the industrial city's priorities reducing the scope (high), delays in purchases because of regional shipping problems (high), frequent work stoppages lowering daily output (medium), and differences between the signed contract value and the work on site (medium).

Data notes

- This-week values compare with the 27-Oct-2026 upload in the W05 folder. The list of this week's major activities in the Photos - Progress Summary sheet is identical to last week's, and the network pipe quantities on the presentation's network slide did not change.
- The report week is the contract week stated in the Milestones sheet ("Current Contract Weeks: 76 of 104"), which matches (03-Nov-2026 – 19-May-2025) ÷ 7. The workbook calls itself report #64; that is not the week number.
- Data dates: weekly report 03-Nov-2026, P6 update 31-Oct-2026. The procurement log uploaded this week is the same 20-Oct-2026 file as last week.
- The same physical-progress rows in the Weekly Progress Report sheet are still wrong: Construction shows 190.1% planned and 207.2% earned; Zone 3 shows 355,540 earned man-hours (the whole project's total) against a 147,160 budget; local roads show 998.7%; telecom and arterial roads show 0% although the P6 export records 16,514 and 287 actual man-hours. The P6 export values were used for these rows.
- The man-hour budget is 458,486 in the total row but 467,288 as the sum of the zones (467,280 in the S-curve sheet).
- The planned 96.6% to date matches neither curve in the Physical-Chart Data sheet (baseline 93.3%, revised plan 95.9% for November). The sheet's last actual entry sits under June 2026 but holds the to-date total (355,636 man-hours), so it changes every week; the March–May 2026 actuals are identical to the revised plan.
- Completion: weekly report 18-May-2027 against P6 27-Oct-2027. The P6 update leaves milestones 3 and 4 (work plan, drawings approval) not started with dates of 31-Oct-2026 and 05-Nov-2026, while the weekly report and presentation show them complete. Last week's uploaded schedule was a different 136-activity revised file.

- The Target schedule sheet and presentation slides 3, 4 and 10 report value-weighted (cost-based) progress labelled as actual or achieved; those figures are not used in this report.
- Contract value is 233,776,077 SAR in the weekly report and 233,575,734 SAR in the presentation. Invoices are unchanged: 37.3M SAR (12 invoices) in the weekly report, 60.6M SAR in the invoice log including the advance payment, 65.1M SAR disbursed in the presentation.
- Manpower: the summary panel still shows 388 labour and 57 staff (445), while the monthly table and the presentation show 332 labour and 66 staff (398) for November.
- Pumps delivered fell from 3 in the 27-Oct presentation to 2 in the 03-Nov presentation; the status text says 2 in both. NCRs closed fell from 53 to 52, so one NCR appears to have been reopened.
- Scope quantities: the progress scope slide is still labelled "15 September update" and its telecom and potable water totals differ from the network slide. The street lighting quantity (53 of 54) has no unit.
- The "Modon PM" field in the weekly report is blank; the PM name is taken from the MODON risk and issue log.

Compiled 05-Nov-2026 from the weekly report uploaded for week 76 (data date 03-Nov-2026), with week 75 (27-Oct-2026) for the weekly changes.
