Playground Initiative for Eastern Region (Arar, Hasa Oasis, Dammam 2nd)

مبادرة الملاعب بالمنطقة الشرقية (عرعر, واحة الاحساء, الدمام الثانية)

CLIENT	CONTRACTOR	CONSULTANT	MODON PM	SITE HANDOVER	CONTRACT COMPLETION
MODON	Profast Company Ltd.	EGIS	Eng. Mohamed Alisa	03-Mar-2026	02-Jan-2027

Scope: football, basketball and padel grounds, an air dome, a service and toilet building, landscape works, parking, and bike and walking paths at three sites: Hasa Oasis, the 2nd Industrial City at Arar and the 2nd Industrial City at Dammam.

Status at a glance

Progress is measured as physical % complete, weighted by budgeted man-hours. The project is at 61.72% against 61.67% planned, on the current plan (SPI 1.00). It gained 2.53% this week against 2.82% planned, so the weekly plan was missed by 0.29%. Hasa Oasis construction is ahead (66.8% against 56.4% planned), Arar construction has slipped to 2.5% behind and procurement is 17.2% behind.

PHYSICAL % COMPLETE

61.72% / 61.67%

plan

● SPI 1.00 +0.05%

PROGRESS THIS WEEK

+2.53% / +2.82%

plan

▼ 0.29% below the weekly plan

CONTRACT TIME ELAPSED

82.3% · day 251 of 305

▼ Forecast finish 15-Mar-2027

INVOICED TO DATE (GROSS)

17.9% · 5.37M SAR

7 invoices, last period ends 04-Nov-2026

Project completion is forecast 72 days late.

The weekly report and the P6 update (data date 09-Nov-2026) both forecast completion on 15-Mar-2027, against the contract completion date of 02-Jan-2027. This is 16 days later than last week's forecast of 27-Feb-2027. P6 shows −57 days of float on project completion and 219 open activities with negative float, against 258 last week. The three site-completion milestones are now forecast for 23-Feb (Hasa Oasis), 06-Mar (Dammam) and 09-Mar-2027 (Arar); Arar moved 26 days later this week. Supply of the air dome remains the cause of delay named in the weekly summary. The original baseline called for 91.5% by the end of November.

Site photos this week

Four photos from the Weekly Photos sheet of the 09-Nov-2026 weekly report. Of the other two, one is under 600 px wide and the other, captioned as the air dome entrance foundation at Arar, shows interlock paving instead, so neither is shown. Select a photo to view it larger, then use the arrows to move between photos.



Interlock paving, Arar

Interlock laid along the grounds, with the service building and lighting poles behind.




Slab on grade for the tartan area, Hasa Oasis

Concrete slab poured as the base for the tartan floor, with newly planted trees around it.



Bike and walking path, Hasa Oasis

Compaction and levelling for the path. Stamped 09-Nov-2026, 13:03, Al-Hofuf, Al-Ahsa.

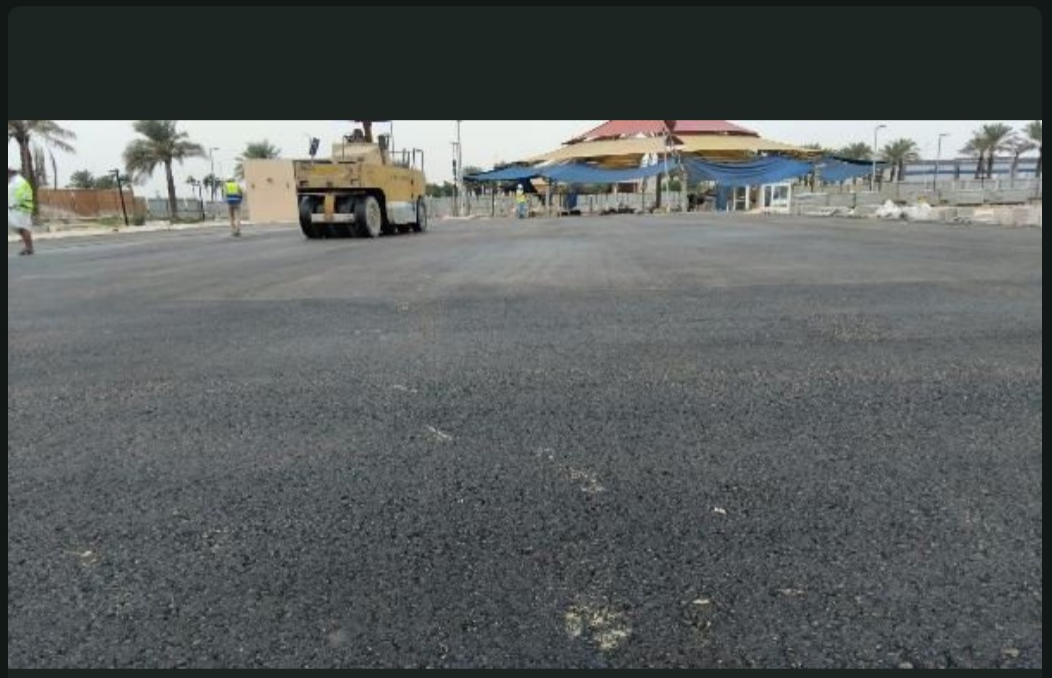


Asphalt layer, football ground, Dammam

Asphalt laid on the football ground.

Progress S-curve

Cumulative physical progress (man-hour weighted), month-end values; the last actual point is the 09-Nov data date. Source: Physical-Chart Data sheet and Weekly Progress Report sheet, weekly report 09-Nov-2026.

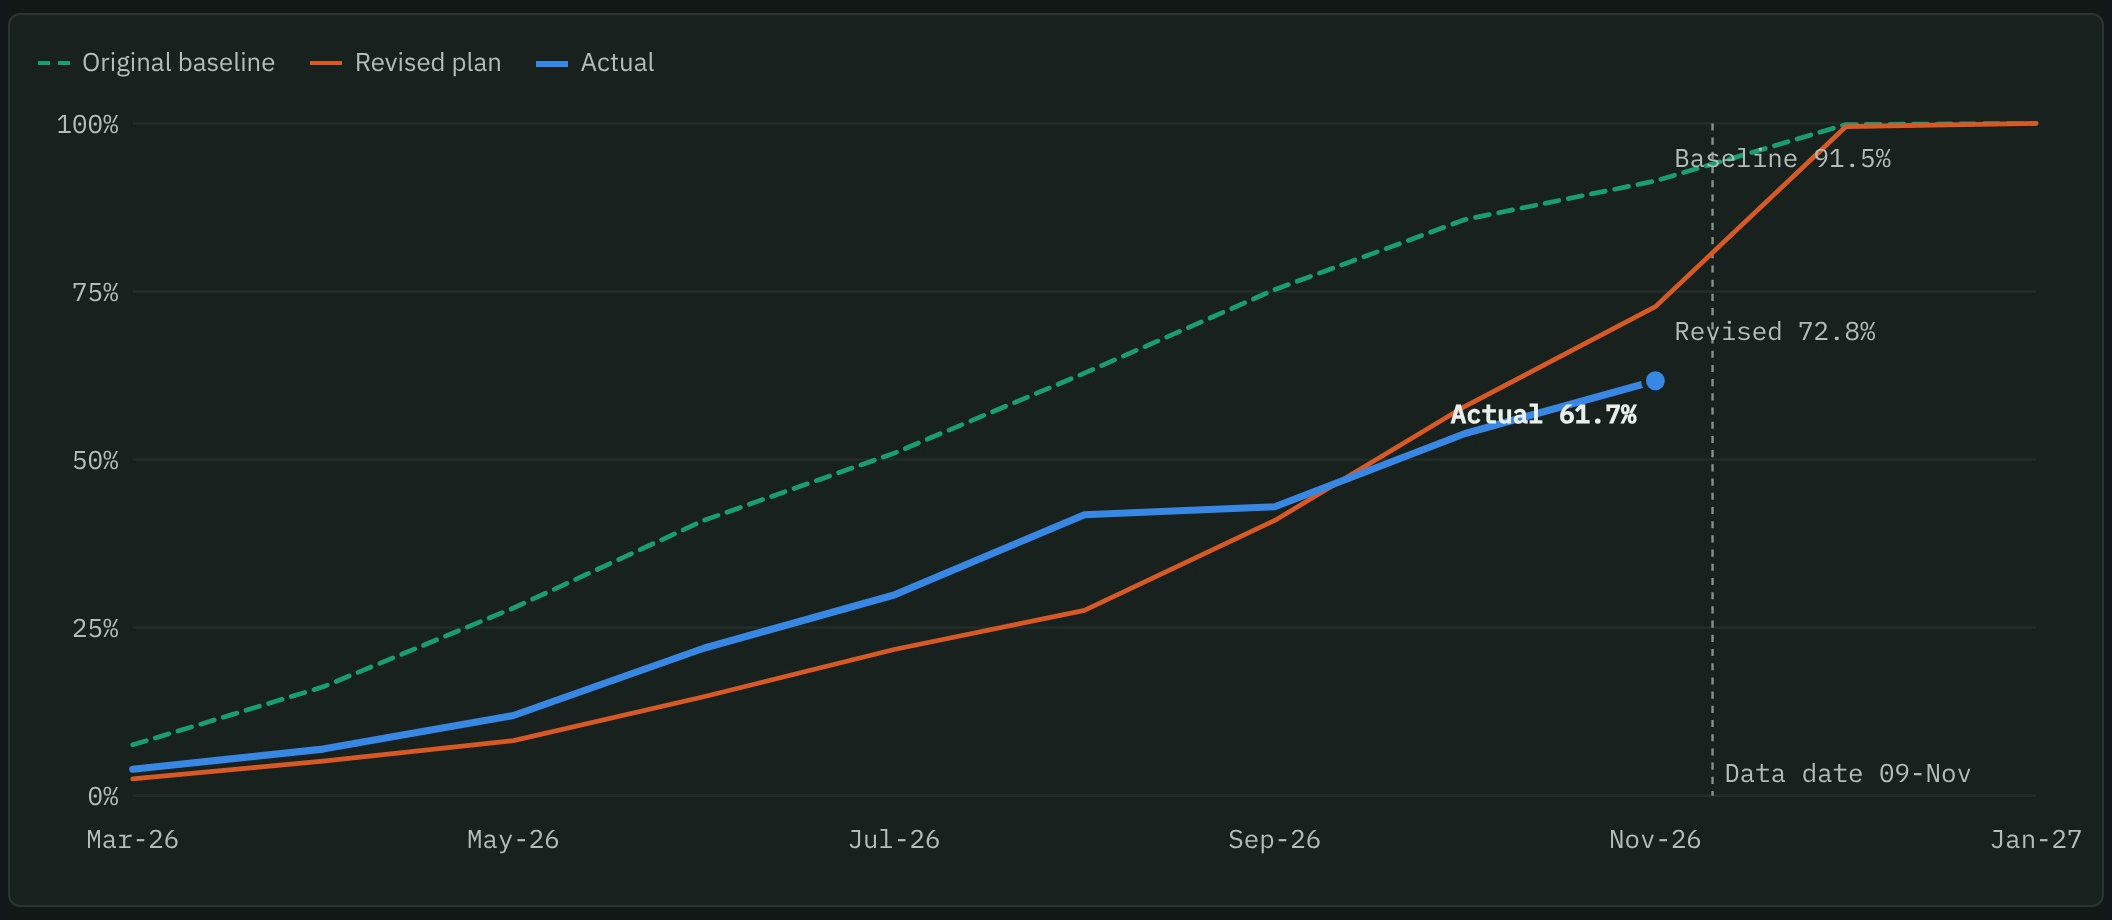

WEEK ENDING	PLANNED %	ACTUAL %	VARIANCE	GAINED THIS WEEK	SPI
12-Oct-2026	—	46.9	—	+0.9	—
19-Oct-2026	50.1	50.3	+0.2	+3.4	1.00
26-Oct-2026	53.7	53.9	+0.2	+3.6	1.00
26-Oct-2026 (restated)	53.7	55.3	+1.6	—	1.03
02-Nov-2026	58.9	59.2	+0.3	+3.9	1.01
09-Nov-2026	**61.7**	**61.7**	**+0.05**	**+2.5**	**1.00**

Rows up to 02-Nov come from the earlier weekly reports (W05 and W06 MD Files). This week's to-date figure, 258,411 man-hours, is last week's 247,833 plus the 10,578 earned this week, so no restatement was needed. The Physical-Chart Data sheet now matches the headline figure.

Progress by phase

Physical progress to date by WBS, weighted by budgeted man-hours. Source: Weekly Progress Report sheet, 09-Nov-2026.


PHASE	WEIGHT	PLANNED	ACTUAL	VARIANCE	SPI	STATUS
Mobilization	3.0%	100.0%	100.0%	0.0%	1.00	✓ Complete
Engineering	5.0%	98.4%	99.8%	+1.4%	1.01	▲ Ahead
Procurement	12.0%	88.2%	71.0%	−17.2%	0.80	▼ Behind
Construction	75.0%	57.6%	60.3%	+2.7%	1.05	▲ Ahead
Construction: Arar	24.9%	57.5%	55.0%	−2.5%	0.96	▼ Slightly behind
Construction: Hasa Oasis	25.0%	56.4%	66.8%	+10.4%	1.18	▲ Ahead
Construction: Dammam	25.0%	58.8%	59.0%	+0.2%	1.00	● On plan
Testing & commissioning	3.0%	0.0%	0.0%	0.0%	–	○ Not started

PHASE	WEIGHT	PLANNED	ACTUAL	VARIANCE	SPI	STATUS
Close-out	2.0%	0.0%	0.0%	0.0%	–	○ Not started
Total	100%	**61.67%**	**61.72%**	**+0.05%**	**1.00**	● On plan

By site, all phases included: Arar 58.5% against 63.0% planned, Hasa Oasis 67.7% against 62.9%, Dammam 62.8% against 62.9%. The P6 update has 2,150 activities: 1,876 completed, 29 in progress and 245 not started. Its scheduled finish is 15-Mar-2027, 72 days after the contract date.

Scope of work: quantities

Total quantity and quantity executed to date for the main BOQ items, all three sites combined, from the Major Quantities sheet of the 09-Nov-2026 weekly report. The sheet does not split quantities by site. "This week" is the change from the 02-Nov-2026 report; every quantity in the sheet is unchanged.

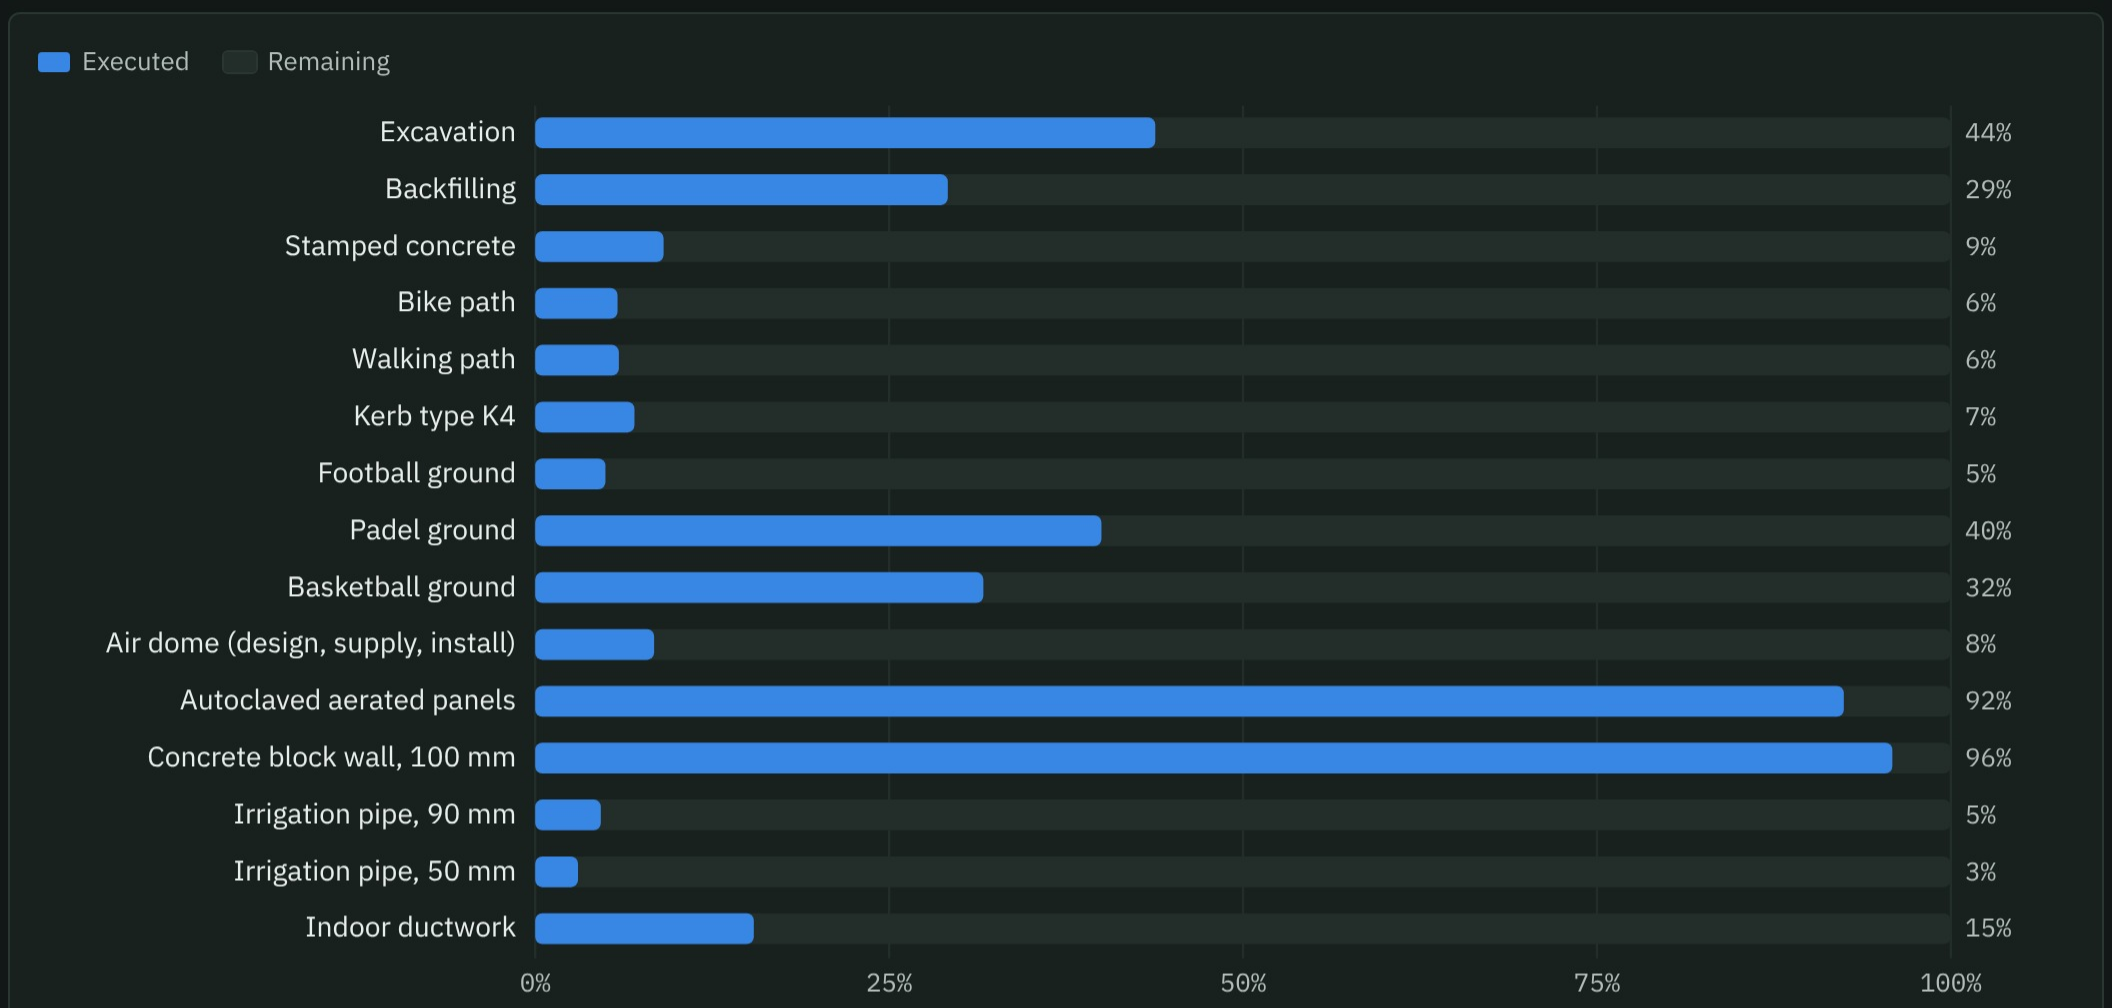

SCOPE ITEM	ZONE	UNIT	TOTAL	FINISHED	THIS WEEK	REMAINING	% FINISHED	BACKFILLED
Excavation	All sites	m³	10,295	4,510	0	5,785	43.8%	–
Backfilling	All sites	m³	10,266	2,992	0	7,274	29.1%	–
Stamped concrete	All sites	m²	1,800	163.3	0	1,637	9.1%	–
Bike path	All sites	m²	2,300	133.8	0	2,166	5.8%	–
Walking path	All sites	m²	2,200	130.1	0	2,070	5.9%	–
Kerb type K4	All sites	LM	9,080	636.7	0	8,443	7.0%	–
Football ground	All sites	m²	3,000	148.9	0	2,851	5.0%	–
Padel ground	All sites	m²	600	240	0	360	40.0%	–
Basketball ground	All sites	m²	1,530	484.4	0	1,046	31.7%	–
Air dome (design, supply, install)	All sites	item	3	0.3	0	2.7	8.4%	–
Autoclaved aerated panels	All sites	m²	750	693.3	0	56.7	92.4%	–
Concrete block wall, 100 mm	All sites	m²	135	129.4	0	5.6	95.9%	–

SCOPE ITEM	ZONE	UNIT	TOTAL	FINISHED	THIS WEEK	REMAINING	% FINISHED	BACKFILLED
Irrigation pipe, 90 mm	All sites	LM	750	34.8	0	715.2	4.6%	–
Irrigation pipe, 50 mm	All sites	LM	350	10.6	0	339.4	3.0%	–
Indoor ductwork	All sites	kg	300	46.3	0	253.7	15.4%	–

Status by site this week

Arar: interlock being laid on the football, basketball and padel grounds, the air dome foundation poured and its waterproofing under way, lighting fixtures installed. Hasa Oasis: slab on grade poured for the tartan area, bike and walking paths levelled for the asphalt layer, irrigation sprinklers and bubblers being installed, earthing finished in the service building, trees being planted. Dammam: an asphalt layer laid on the football ground and interlock laid between the grounds. Tree pits are being excavated and trees planted at all three sites.

Quantities not updated

The Major Quantities sheet is identical to the last two weeks', although the weekly summary reports asphalt, interlock and tree planting this week. Items reported beyond their BOQ total (150 mm uPVC external wastewater pipe 126.81 of 50 m, plastering 551.07 of 471 m², foundation waterproofing 101.55 of 60 m², slab on grade 46.17 of 45 m³, polyethylene sheet and anti-termite 288.75 of 270 m²) are left out of the chart and table.

Milestones

The weekly report's Milestones sheet and the P6 update give the same forecast dates. Float is from the P6 update (data date 09-Nov-2026).

MILESTONE	BASELINE	WEEKLY REPORT FORECAST	P6 UPDATE FORECAST	P6 FLOAT (DAYS)	STATUS
Project commencement	03-Mar-2026	03-Mar-2026	03-Mar-2026 (actual)	–	✓ Done
Baseline programme approval	01-Apr-2026	04-Apr-2026	04-Apr-2026 (actual)	–	✓ Done
Completion of mobilization	02-Apr-2026	02-Apr-2026	02-Apr-2026 (actual)	–	✓ Done
Completion of levelling works	02-Apr-2026	02-May-2026	02-May-2026 (actual)	–	✓ Done
Completion of engineering	02-May-2026	06-Jan-2027	06-Jan-2027	−7	▼ Late
Completion of toilet building	02-Aug-2026	23-Feb-2027	23-Feb-2027	−44	▼ Late
Completion of playground area	24-Aug-2026	23-Feb-2027	23-Feb-2027	−44	▼ Late
Completion of natural landscape works	02-Nov-2026	09-Mar-2027	09-Mar-2027	−55	▼ Late
Completion of Arar works	21-Dec-2026	09-Mar-2027	09-Mar-2027	−55	▼ Late
Completion of Hasa Oasis works	21-Dec-2026	23-Feb-2027	23-Feb-2027	−43	▼ Late
Completion of Dammam works	21-Dec-2026	06-Mar-2027	06-Mar-2027	−52	▼ Late
Completion of testing & commissioning	21-Dec-2026	09-Mar-2027	09-Mar-2027	−55	▼ Late
Project completion	02-Jan-2027	15-Mar-2027	15-Mar-2027	−57	▼ Late

Arar landscape, late purchase orders and the air dome drive the finish date.

The most negative float in P6 (−57 days) now sits at Arar: the purchase orders and deliveries for pavement markings and marking paint, the track surface delivery, and the benches, precast seats, trash bins and traffic signs that follow. At Dammam (−52 days) the purchase orders for distribution boards and power cables, the padel wire mesh delivery, stamped concrete, furniture and MEP testing of the landscape works are critical. Air dome membrane deliveries now run from 09-Nov to 31-Dec-2026 and membrane installation from 05-Jan to 28-Jan-2027, with −9 to −42 days of float. MEP testing and commissioning is forecast from 28-Jan to 09-Mar-2027.

Procurement of key materials

Share of total quantity delivered to site. Source: supply tracking file (ملف التوريدات) dated 26-Oct-2026, the latest uploaded; no new supply file came with this week's report.



The weekly report's procurement summary is unchanged for a second week: 119 materials, 116 purchase orders issued, 3 still to issue, 99 materials on site and 20 still to arrive. Procurement physical progress rose from 65.4% to 71.0% against 88.2% planned.

Air dome: nothing delivered yet


At 26-Oct, purchase orders were issued and advance payments made for the membrane, anchors, L-profiles, lighting, ventilation, generators, ATS, doors, fire-fighting, panels and electrical material, with supply scheduled from 01-Nov to 05-Dec-2026. The 18 package units were in final approval and the entrance steel and curtain wall in manufacture. P6 now places the first membrane delivery from 09-Nov-2026 and the last by 31-Dec-2026.

Landscape, path and ground surfaces

Trees (298), lawn (7,030 m²), tartan floor (510 m²), bike and walking path surfaces (4,281 m²) and the football and padel ground surfaces were ordered and paid, with supply due between 29-Oct and 30-Nov-2026. Trees are now being planted at all three sites. Lighting fixtures (105) were paid and ready to supply; LV panel boards (9) were in manufacture.

Manpower

Monthly head count on site (manual and non-manual), planned vs actual. Source: Manpower sheet. November is the month to the 09-Nov data date.

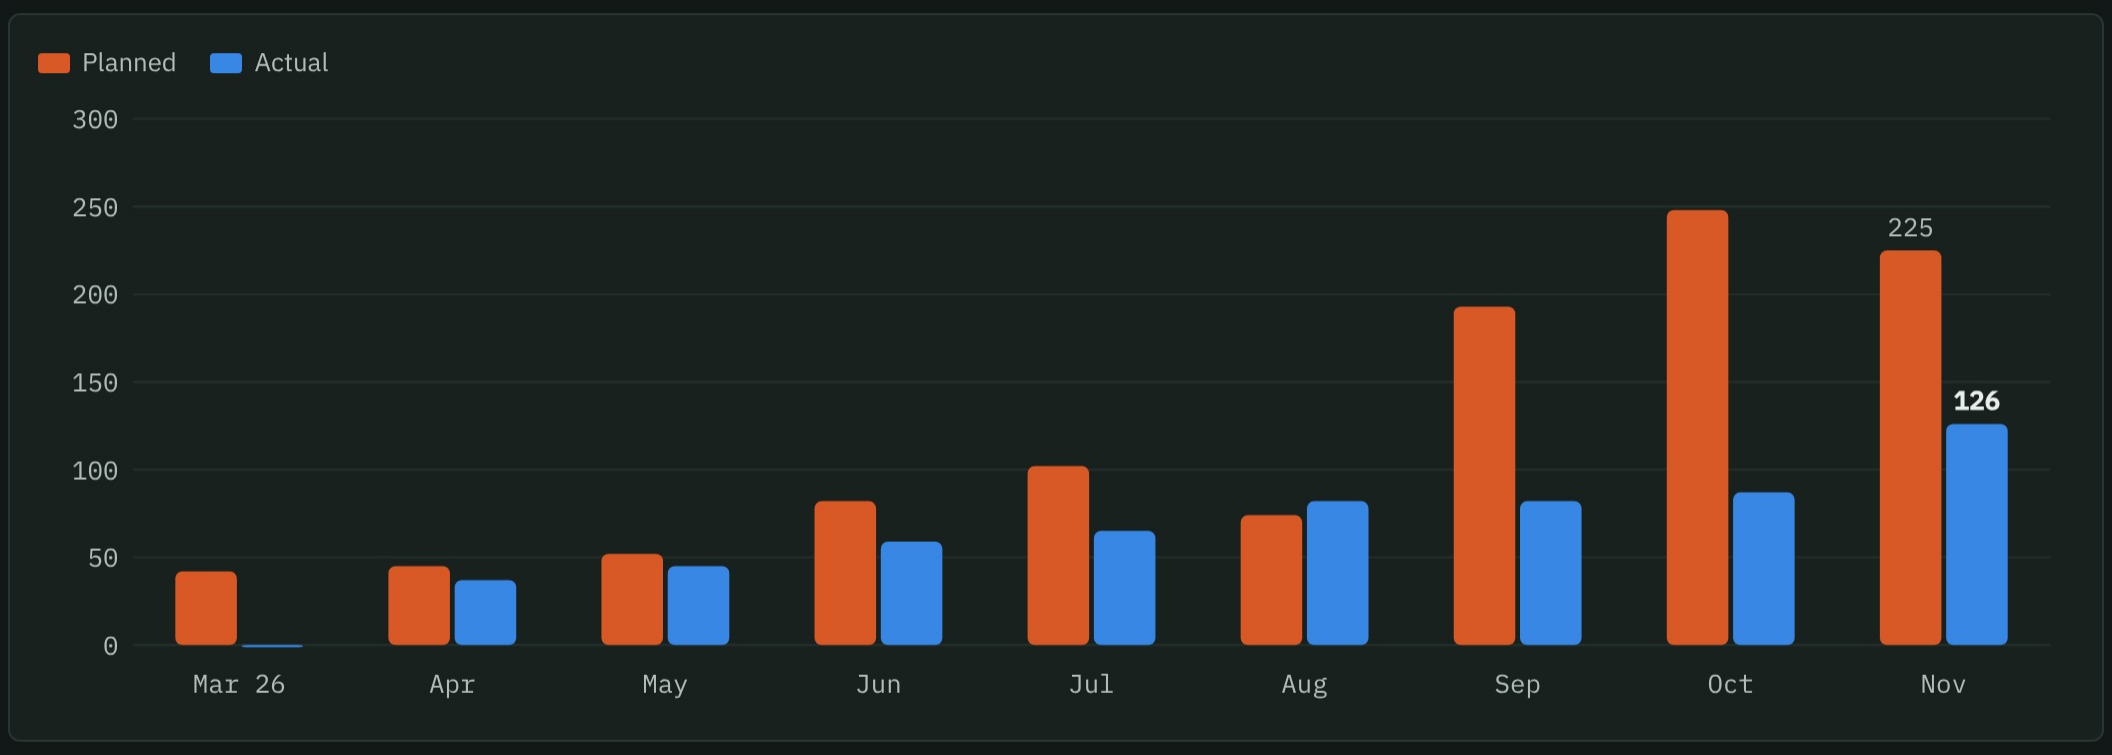

November head count is 126 against 225 planned (–44%): 107 workers against 206 planned and 19 staff as planned. Last week's report showed 75 workers. Equipment on site is 13 against 35 planned. The plan rises to 380 in December 2026.

Cost and invoicing

Contract value

Playground works	20,775,269
Site works	5,722,500
Service buildings	3,500,083
Contract value (excl. VAT)	**29,997,852**
Contract value incl. 15% VAT	34,497,529
Change orders	0

All values in SAR, from the Progress Summary and Invoice Log sheets. No change orders are registered.

Invoices

Invoices submitted	7
Gross value	5,374,032
Approved by MODON PM (5 invoices)	3,673,916
Paid (3 invoices)	2,178,751
Deductions and penalties	59,000
Net incl. VAT	6,121,136
FIR value to date	6,384,884

Invoice 7 (872,505 SAR gross, 21-Oct to 04-Nov-2026) was submitted and approved by the consultant on 04-Nov-2026. Invoicing is 17.9% of the contract value against 61.72% physical progress; approved field inspections are 21.3%. No advance payment or retention is recorded.

Health, safety and quality

Safety Score 0.89

Safe man-hours (cumulative)	47,491
Man-hours this week	1,575
Lost-time injuries	0
Fatalities	0
First-aid cases	0
Near misses	0
Inductions / toolbox talks	37 / 115
Internal audits	5

Quality Score 0.86

FIRs issued / closed / pending	1,012 / 989 / 23
MIRs issued / closed / pending	204 / 192 / 12
NCRs issued / closed / pending	29 / 27 / 2
Site instructions issued / closed / pending	16 / 6 / 10
Shop drawing submittals (134 planned)	159
Material submittals (119 planned)	140

Cumulative counts from the Quality-Stat sheet. This week 29 FIRs and 10 MIRs were issued; no new NCRs or site instructions. All pending items are less than 10 days old.

Open issues and risks

ISSUE	OWNER	DETAIL
Air dome supply	Contractor	Late manufacture and supply of the air dome is the cause of delay named in the weekly summary. The risk register rates late delivery of this long-lead item as high likelihood and very high impact. Membrane delivery and installation run with negative float.
Arar falling behind	Contractor	Arar construction is 2.5% behind plan (1.3% last week), and its completion forecast moved 26 days to 09-Mar-2027. Its pavement-marking, track-surface and furniture activities carry the project's most negative float.
Procurement behind plan	Contractor	Procurement is at 71.0% against 88.2% planned (physical). Twenty materials are not yet on site, three purchase orders are still to be issued, and P6 shows purchase orders for pavement markings, marking paint, CCTV, distribution boards and power cables with −51 to −57 days of float.
Shop drawing submittals	Contractor	Open since 03-Apr-2026. The expected closure of 29-Oct-2026 has passed and the log has not been updated. Two shop drawings remain to be submitted.
Manpower and equipment	Contractor	107 workers on site against 206 planned for November, and 13 pieces of equipment against 35 planned, while the plan calls for 361 workers in December.
Interfaces between finishes and the air dome	Contractor	The supply file ties the final layer of the paths and grounds to the air dome finishing, to avoid damage; these surfaces were 60% paid but not delivered at 26-Oct.

No new issues were logged this week. Other open risks in the register cover site access, confined spaces, material storage, equipment certification, work at height, heat and traffic separation.

Data notes

- Week number: the Milestones sheet states "Current Contract Weeks: 28 of 44", which is again the report number (WPR-28). From site handover on 03-Mar-2026 to the 09-Nov-2026 data date is 251 days, week 35, one week after last week's report (week 34).
- The MODON summary files (Look Ahead, الأعمال المنفذة ونسب الإنجاز, الأعمال المنفذه خلال الإسبوع) and the Progress Summary sheet label cost-based progress as actual progress. Those figures are not used here.
- The file الأعمال المنفذه خلال الإسبوع still carries details of another project: project manager عبد الله الشنيفي, contractor شركة الانجاز, start 24-Nov-2025, contract end 23-May-2026 and sector القطاع الأوسط. The Look Ahead file names the consultant (شركة ايجس) as the contractor.
- No supply file (ملف التوريدات) was uploaded this week, and the procurement log and the report's Procurement sheet are identical to the last two weeks'. The procurement chart therefore still shows the 26-Oct-2026 position.
- The Major Quantities sheet is unchanged for the third week running, so the this-week column shows 0 although asphalt, interlock and tree planting are reported. Several items exceed their BOQ quantity and "Plan To Date" equals the full quantity for every item.
- The Schedule sheet still counts 1,835 completed activities (245 not started, 29 in progress, 2,109 in all) against a total of 2,150; the P6 update has 1,876 completed.
- The milestone table on the Weekly Progress Report sheet still has its names shifted by one row against the Milestones sheet, and the Milestones sheet marks "Completion of Engineering" as actual although its forecast is 06-Jan-2027.
- Of the six weekly photos, the interlock photo at Dammam is 599 px wide, under the 600 px minimum, and the photo captioned "Pouring of entrance foundation for Air dome (Arar)" shows interlock paving and a lighting pole, not a foundation. Neither is shown.
- Several summary cells in the DB and Invoice Log sheets show #REF! errors.

Compiled 10-Nov-2026 from the weekly report with data date 09-Nov-2026 (WPR-28), compared with the 02-Nov-2026 report (WPR-27).
