
egis ENJAZCO

MKH2-02-003 - Completion of Infrastructure Works at the Second Industrial City in Makkah UP 34
Remaining Work

MODON مدن

Activity ID	Activity Name	Original Duration	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Schedule % Complete	Performance % Complete	Variance - BL Project Finish Date
MKH2-02-003 - Completion of Infrastr		421	18-Apr-26	14-Aug-27	08-Apr-26 A	05-Sep-27	3,120,889.61	5,043,487.17	15,779,557.83	19.78%	31.96%	-19
KEY MILESTONES		190	14-Dec-26	14-Aug-27	18-Jan-27	05-Sep-27	0.00	0.00	0.00	0%	0%	-19
GENERAL MILESTONES		0	14-Aug-27	14-Aug-27	05-Sep-27	05-Sep-27	0.00	0.00	0.00	0%	0%	-19
MKH2-02-003-M	Project Completion	0		14-Aug-27		05-Sep-27	0.00	0.00	0.00	0%	0%	-19
CONTRACTUAL MILESTONE		190	14-Dec-26	14-Aug-27	18-Jan-27	05-Sep-27	0.00	0.00	0.00	0%	0%	-19
MKH2-02-003-M	Completion of Road Works	0		14-Dec-26		18-Jan-27	0.00	0.00	0.00	0%	0%	-30
MKH2-02-003-M	Completion of Open Drain Channel	0		14-Jun-27		06-Jul-27	0.00	0.00	0.00	0%	0%	-19
MKH2-02-003-M	Completion of All Works	0		14-Aug-27		05-Sep-27	0.00	0.00	0.00	0%	0%	-19
MKH2-02-003-M	Final Handover	0		14-Aug-27		05-Sep-27	0.00	0.00	0.00	0%	0%	-19
PROCUREMENT		206	18-Apr-26	16-Aug-26	08-Apr-26 A	07-Jan-27	765,081.00	433,545.90	765,081.00	100%	56.67%	-123
SHORT LEAD ITEM		206	18-Apr-26	14-Jun-26	08-Apr-26 A	20-Dec-26	765,081.00	433,545.90	765,081.00	100%	56.67%	-161
ROAD WORKS-CIVIL		206	18-Apr-26	14-Jun-26	08-Apr-26 A	20-Dec-26	765,081.00	433,545.90	765,081.00	100%	56.67%	-161
BITUMINOUS BASE & WEARING COURSE		25	18-Apr-26	16-May-26	08-Apr-26 A	22-Nov-26	255,027.00	204,021.60	255,027.00	100%	80%	-159
MKH2-02-003-	Material Delivery for 1st lot to the Site	25	18-Apr-26	16-May-26	08-Apr-26 A	22-Nov-26	255,027.00	204,021.60	255,027.00	100%	80%	-159
INTERLOCKING PAVING BLOCKS		22	17-May-26	14-Jun-26	15-Jul-26 A	17-Dec-26	255,027.00	229,524.30	255,027.00	100%	90%	-159
MKH2-02-003-	Material Delivery for 1st lot of Interlock	22	17-May-26	14-Jun-26	15-Jul-26 A	17-Dec-26	255,027.00	229,524.30	255,027.00	100%	90%	-159
PAVEMENT MARKING		46	19-Apr-26	14-Jun-26	28-Oct-26	20-Dec-26	255,027.00	0.00	255,027.00	100%	0%	-161
MKH2-02-003-	Material Fabrication for Pavement Ma	24	19-Apr-26	16-May-26	28-Oct-26	24-Nov-26	0.00	0.00	0.00	100%	0%	-161
MKH2-02-003-	Material Delivery for 1st lot of Paveme	22	17-May-26	14-Jun-26	25-Nov-26	20-Dec-26	255,027.00	0.00	255,027.00	100%	0%	-161
LONG LEAD ITEM		28	15-Jul-26	16-Aug-26	20-May-26 A	07-Jan-27	0.00	0.00	0.00	0%	0%	-123
ELECTRICAL POWER		9	15-Jul-26	25-Jul-26	20-May-26 A	29-Dec-26	0.00	0.00	0.00	0%	0%	-134
LV-CABLES		9	15-Jul-26	25-Jul-26	20-May-26 A	29-Dec-26	0.00	0.00	0.00	0%	0%	-134
MKH2-02-003-	Staging Time for Low Voltage Cables	9	15-Jul-26	25-Jul-26	20-May-26 A	29-Dec-26	0.00	0.00	0.00	100%	60%	-134
STREET LIGHTING		28	23-Jul-26	16-Aug-26	10-Jun-26 A	07-Jan-27	0.00	0.00	0.00	0%	0%	-123
POLES		9	23-Jul-26	02-Aug-26	10-Jun-26 A	05-Nov-26	0.00	0.00	0.00	0%	0%	-81
MKH2-02-003-	Staging Time for Street Light poles	9	23-Jul-26	02-Aug-26	10-Jun-26 A	05-Nov-26	0.00	0.00	0.00	100%	0%	-81
LUMINAIRE		9	06-Aug-26	16-Aug-26	10-Jun-26 A	07-Jan-27	0.00	0.00	0.00	0%	0%	-123
MKH2-02-003-	Staging Time for Street Lighting Lumi	9	06-Aug-26	16-Aug-26	10-Jun-26 A	07-Jan-27	0.00	0.00	0.00	100%	0%	-123
CONSTRUCTION PHASE		347	23-Jun-26	14-Jun-27	20-Apr-26 A	17-Jul-27	2,355,808.61	4,349,813.69	9,811,925.23	24.01%	44.33%	-28
ROADS		332	15-Jul-26	07-Jun-27	20-Apr-26 A	17-Jul-27	2,322,308.61	3,840,250.00	8,308,253.91	27.95%	46.22%	-34
ARTERIAL-03 (2+510 to 4+267.54)		62	21-Nov-26	15-Mar-27	09-Jan-27	25-Mar-27	0.00	0.00	983,479.60	0%	0%	-9
ARTERIAL-03-ROAD		62	21-Nov-26	15-Mar-27	09-Jan-27	25-Mar-27	0.00	0.00	983,479.60	0%	0%	-9
ROADS & ROUNDABOUT		62	21-Nov-26	15-Mar-27	09-Jan-27	25-Mar-27	0.00	0.00	983,479.60	0%	0%	-9
ASPHALT WORKS		42	21-Nov-26	07-Jan-27	09-Jan-27	27-Feb-27	0.00	0.00	870,852.60	0%	0%	-42
MKH2-02-0(	Tack coat at ARTERIAL-03	21	21-Nov-26	14-Dec-26	09-Jan-27	01-Feb-27	0.00	0.00	87,046.40	0%	0%	-42
MKH2-02-0(	Bituminous concrete wearing course	21	15-Dec-26	07-Jan-27	02-Feb-27	27-Feb-27	0.00	0.00	783,806.20	0%	0%	-42
FINISHING WORKS		20	16-Feb-27	15-Mar-27	28-Feb-27	25-Mar-27	0.00	0.00	112,627.00	0%	0%	-9
MKH2-02-0(	Pavement markings [Road-1 -ARTE	10	16-Feb-27	28-Feb-27	28-Feb-27	14-Mar-27	0.00	0.00	89,847.00	0%	0%	-9
MKH2-02-0(	Installation of Traffic Signs [Road-1 -A	10	01-Mar-27	15-Mar-27	15-Mar-27	25-Mar-27	0.00	0.00	22,780.00	0%	0%	-9
ARTERIAL-04 (0+000 to 1+0.83)		304	15-Jul-26	06-May-27	20-Apr-26 A	12-May-27	1,683,478.14	2,470,971.92	3,603,610.37	46.72%	68.57%	-5
ARTERIAL-04-ROAD		304	15-Jul-26	06-May-27	20-Apr-26 A	12-May-27	1,683,478.14	2,470,971.92	3,603,610.37	46.72%	68.57%	-5
ROADS		262	15-Jul-26	14-Mar-27	20-Apr-26 A	22-Apr-27	1,683,478.14	2,094,301.94	3,176,713.17	52.99%	65.93%	-34
EARTHWORKS & SITE GRADING		48	15-Jul-26	27-Aug-26	20-Apr-26 A	16-Nov-26	1,683,478.14	1,626,659.70	1,683,478.14	100%	96.62%	-68
MKH2-02-0(	Roadway Excavation for cuttings AR	20	15-Jul-26	06-Aug-26	20-May-26 A	05-Nov-26	911,848.83	893,611.85	911,848.83	100%	98%	-77
MKH2-02-0(	Embankments -ARTERIAL-04	18	08-Aug-26	27-Aug-26	20-Apr-26 A	16-Nov-26	771,629.31	733,047.85	771,629.31	100%	95%	-68
ASPHALT WORKS		34	15-Dec-26	23-Jan-27	02-Feb-27	17-Mar-27	0.00	0.00	738,728.60	0%	0%	-42
MKH2-02-0(	Tack coat at ARTERIAL-04	14	15-Dec-26	30-Dec-26	02-Feb-27	17-Feb-27	0.00	0.00	73,834.00	0%	0%	-42
MKH2-02-0(	Bituminous concrete wearing course	20	31-Dec-26	23-Jan-27	18-Feb-27	17-Mar-27	0.00	0.00	664,894.60	0%	0%	-42
FINISHING WORKS		65	24-Jan-27	14-Mar-27	05-Sep-26 A	22-Apr-27	0.00	467,642.25	754,506.43	0%	61.98%	-34
MKH2-02-0(	Installation of Precast Concrete curb	8	24-Jan-27	01-Feb-27	05-Sep-26 A	27-Mar-27	0.00	186,715.94	266,737.05	0%	70%	-42

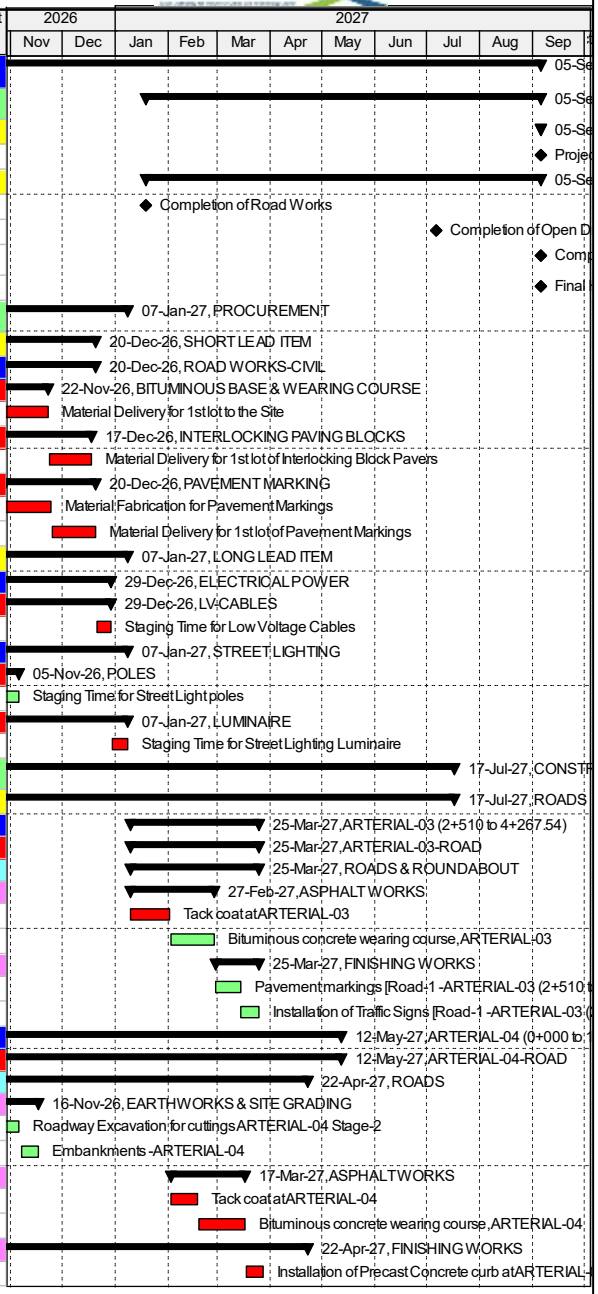

Actual Work | Critical Remaining Work | Remaining Work | Milestone


Date	Revision	Checked	Approved

egis ENJAZCO

MKH2-02-003 - Completion of Infrastructure Works at the Second Industrial City in Makkah UP 34
Remaining Work

MODON مدن

Activity ID	Activity Name	Original Duration	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Schedule % Complete	Performance % Complete	Variance - BL Project Finish Date
MKH2-02-0(	60mm thick - Interlocking block pave	12	02-Feb-27	15-Feb-27	19-Sep-26 A	31-Mar-27	0.00	280,926.31	401,323.30	0%	70%	-34
MKH2-02-0(	Pavement markings [Road-2 -ARTE	9	16-Feb-27	27-Feb-27	01-Apr-27	11-Apr-27	0.00	0.00	76,195.08	0%	0%	-34
MKH2-02-0(	Installation of Traffic Signs [Road-2 -A	10	28-Feb-27	14-Mar-27	12-Apr-27	22-Apr-27	0.00	0.00	10,251.00	0%	0%	-34
ELECTRICAL WORKS (MKH2-01-007-DAR-TS8-0-		119	23-Jan-27	06-May-27	18-Aug-26 A	12-May-27	0.00	376,669.98	426,897.20	0%	88.23%	-5
LV NETWORKS		14	23-Jan-27	07-Feb-27	19-Jan-27	03-Feb-27	0.00	0.00	8,040.00	0%	0%	3
MKH2-02-0(	Supply and installation of KWH mete	14	23-Jan-27	07-Feb-27	19-Jan-27	03-Feb-27	0.00	0.00	8,040.00	0%	0%	3
LV CABLES		13	23-Feb-27	09-Mar-27	24-Aug-26 A	18-Feb-27	0.00	97,360.38	108,178.20	0%	90%	15
MKH2-02-0(	Installation of Low Voltage Cables -A	13	23-Feb-27	09-Mar-27	24-Aug-26 A	18-Feb-27	0.00	97,360.38	108,178.20	0%	90%	15
STREET LIGHTING NETWORK INCLUDING ALL		29	14-Mar-27	13-Apr-27	18-Aug-26 A	06-May-27	0.00	276,897.60	307,664.00	0%	90%	-20
MKH2-02-0(	Installation of Lighting Poles 2-Arms /	15	14-Mar-27	30-Mar-27	18-Aug-26 A	09-Mar-27	0.00	197,784.00	219,760.00	0%	90%	15
MKH2-02-0(	Installation of Lighting Luminaires for	12	31-Mar-27	13-Apr-27	22-Aug-26 A	06-May-27	0.00	79,113.60	87,904.00	0%	90%	-20
EARTHING		20	14-Apr-27	06-May-27	30-Sep-26 A	12-May-27	0.00	2,412.00	3,015.00	0%	80%	-5
MKH2-02-0(	Installation of Earthing System for AR	20	14-Apr-27	06-May-27	30-Sep-26 A	12-May-27	0.00	2,412.00	3,015.00	0%	80%	-5
CONNECTION TO 5th RING ROAD (IF-0+000 to 1+25		203	02-Sep-26	07-Jun-27	23-Sep-26 A	17-Jul-27	586,662.15	1,219,924.13	2,514,733.51	23.33%	48.51%	-34
EARTHWORKS & SITE GRADING		34	02-Sep-26	21-Oct-26	23-Sep-26 A	08-Nov-26	545,587.43	513,427.89	545,587.43	100%	94.11%	-15
MKH2-02-003-	Embankments -to Road connecting	21	02-Sep-26	27-Sep-26	23-Sep-26 A	01-Nov-26	447,984.02	425,584.82	447,984.02	100%	95%	-30
MKH2-02-003-	Subgrade for Connecting Road to R	21	28-Sep-26	21-Oct-26	30-Sep-26 A	08-Nov-26	97,603.42	87,843.07	97,603.42	100%	90%	-15
ASPHALT WORKS		156	22-Oct-26	10-Apr-27	08-Oct-26 A	23-May-27	41,074.72	706,496.24	1,405,325.00	2.92%	50.27%	-34
MKH2-02-003-	Aggregate base course at to Road c	18	22-Oct-26	11-Nov-26	08-Oct-26 A	14-Nov-26	41,074.72	118,295.20	147,869.00	27.78%	80%	-2
MKH2-02-003-	Prime Coat (MC1) to Road connecti	12	12-Nov-26	25-Nov-26	18-Oct-26 A	28-Nov-26	0.00	66,335.36	82,919.20	0%	80%	-2
MKH2-02-003-	Bituminous base course to Road cor	16	26-Nov-26	14-Dec-26	19-Oct-26 A	16-Dec-26	0.00	521,865.68	745,522.40	0%	70%	-2
MKH2-02-003-	Tack coat at to Road connecting roat	21	16-Feb-27	16-Mar-27	01-Apr-27	25-Apr-27	0.00	0.00	42,746.00	0%	0%	-34
MKH2-02-003-	Bituminous concrete wearing course	21	17-Mar-27	10-Apr-27	26-Apr-27	23-May-27	0.00	0.00	386,268.40	0%	0%	-34
FINISHING WORKS		47	11-Apr-27	07-Jun-27	24-May-27	17-Jul-27	0.00	0.00	563,821.08	0%	0%	-34
MKH2-02-003-	Pavement markings [Road-5 -CONI	16	11-Apr-27	28-Apr-27	24-May-27	10-Jun-27	0.00	0.00	44,236.08	0%	0%	-34
MKH2-02-003-	Installation of Traffic Signs [Road-5 -C	16	29-Apr-27	20-May-27	12-Jun-27	29-Jun-27	0.00	0.00	17,085.00	0%	0%	-34
MKH2-02-003-	Installation of Traffic Signs [Road-5 -C	15	22-May-27	07-Jun-27	30-Jun-27	17-Jul-27	0.00	0.00	502,500.00	0%	0%	-34
RAMP-2-IN (0+000 to 0+400)		211	02-Sep-26	04-May-27	08-Aug-26 A	12-Jun-27	52,168.32	76,358.56	665,903.16	7.83%	11.47%	-30
ROADS		151	02-Sep-26	14-Feb-27	08-Aug-26 A	30-Mar-27	52,168.32	76,358.56	421,523.24	12.38%	18.11%	-34
EARTHWORKS & SITE GRADING		35	02-Sep-26	13-Oct-26	08-Aug-26 A	22-Nov-26	44,872.02	42,226.75	44,872.02	100%	94.1%	-34
MKH2-02-00:	Embankments -RAMP-02-IN	14	02-Sep-26	17-Sep-26	08-Aug-26 A	09-Nov-26	36,838.72	34,996.78	36,838.72	100%	95%	-44
MKH2-02-00:	Subgrade for RAMP-2 IN	21	19-Sep-26	13-Oct-26	13-Aug-26 A	22-Nov-26	8,033.30	7,229.97	8,033.30	100%	90%	-34
ASPHALT WORKS		93	14-Oct-26	23-Jan-27	15-Aug-26 A	28-Feb-27	7,296.30	34,131.81	115,809.50	6.3%	29.47%	-30
MKH2-02-00:	Aggregate base course at RAMP-IN	20	14-Oct-26	05-Nov-26	15-Aug-26 A	15-Dec-26	7,296.30	10,944.45	12,160.50	60%	90%	-34
MKH2-02-00:	Prime Coat (MC1) RAMP-02- IN	14	07-Nov-26	22-Nov-26	31-Aug-26 A	31-Dec-26	0.00	4,727.52	6,753.60	0%	70%	-34
MKH2-02-00:	Bituminous base course for RAMP-0	15	23-Nov-26	09-Dec-26	27-Sep-26 A	18-Jan-27	0.00	18,459.84	61,532.80	0%	30%	-34
MKH2-02-00:	Tack coat at RAMP-2-IN	14	15-Dec-26	30-Dec-26	19-Jan-27	03-Feb-27	0.00	0.00	3,497.40	0%	0%	-30
MKH2-02-00:	Bituminous concrete wearing course	20	31-Dec-26	23-Jan-27	04-Feb-27	28-Feb-27	0.00	0.00	31,865.20	0%	0%	-30
FINISHING WORKS		57	10-Dec-26	14-Feb-27	19-Jan-27	30-Mar-27	0.00	0.00	260,841.72	0%	0%	-34
MKH2-02-00:	Installation of Precast Concrete curb	14	10-Dec-26	26-Dec-26	19-Jan-27	03-Feb-27	0.00	0.00	98,791.50	0%	0%	-34
MKH2-02-00:	60mm thick - Interlocking block pave	14	27-Dec-26	11-Jan-27	04-Feb-27	20-Feb-27	0.00	0.00	148,157.10	0%	0%	-34
MKH2-02-00:	Pavement markings [Road-3 -RAMI	14	12-Jan-27	27-Jan-27	21-Feb-27	09-Mar-27	0.00	0.00	3,642.12	0%	0%	-34
MKH2-02-00:	Installation of Traffic Signs [Road-3 -R	15	28-Jan-27	14-Feb-27	14-Mar-27	30-Mar-27	0.00	0.00	10,251.00	0%	0%	-34
ELECTRICAL WORKS (MKH2-01-007-DAR-TS8-0-S		83	24-Jan-27	04-May-27	01-Mar-27	12-Jun-27	0.00	0.00	244,379.92	0%	0%	-30
LV CABLES		21	24-Jan-27	16-Feb-27	01-Mar-27	28-Mar-27	0.00	0.00	80,162.92	0%	0%	-30
MKH2-02-00:	Installation of Low Voltage Cables -R	21	24-Jan-27	16-Feb-27	01-Mar-27	28-Mar-27	0.00	0.00	80,162.92	0%	0%	-30
STREET LIGHTING NETWORK INCLUDING ALL		41	17-Feb-27	10-Apr-27	29-Mar-27	18-May-27	0.00	0.00	163,212.00	0%	0%	-30
MKH2-02-00:	Installation of Lighting Poles 1-Arms I	21	17-Feb-27	17-Mar-27	29-Mar-27	21-Apr-27	0.00	0.00	124,352.00	0%	0%	-30
MKH2-02-00:	Installation of Lighting Luminaires for	20	18-Mar-27	10-Apr-27	22-Apr-27	18-May-27	0.00	0.00	38,860.00	0%	0%	-30
EARTHING		21	11-Apr-27	04-May-27	19-May-27	12-Jun-27	0.00	0.00	1,005.00	0%	0%	-30
MKH2-02-00:	Installation of Earthing System for RA	21	11-Apr-27	04-May-27	19-May-27	12-Jun-27	0.00	0.00	1,005.00	0%	0%	-30

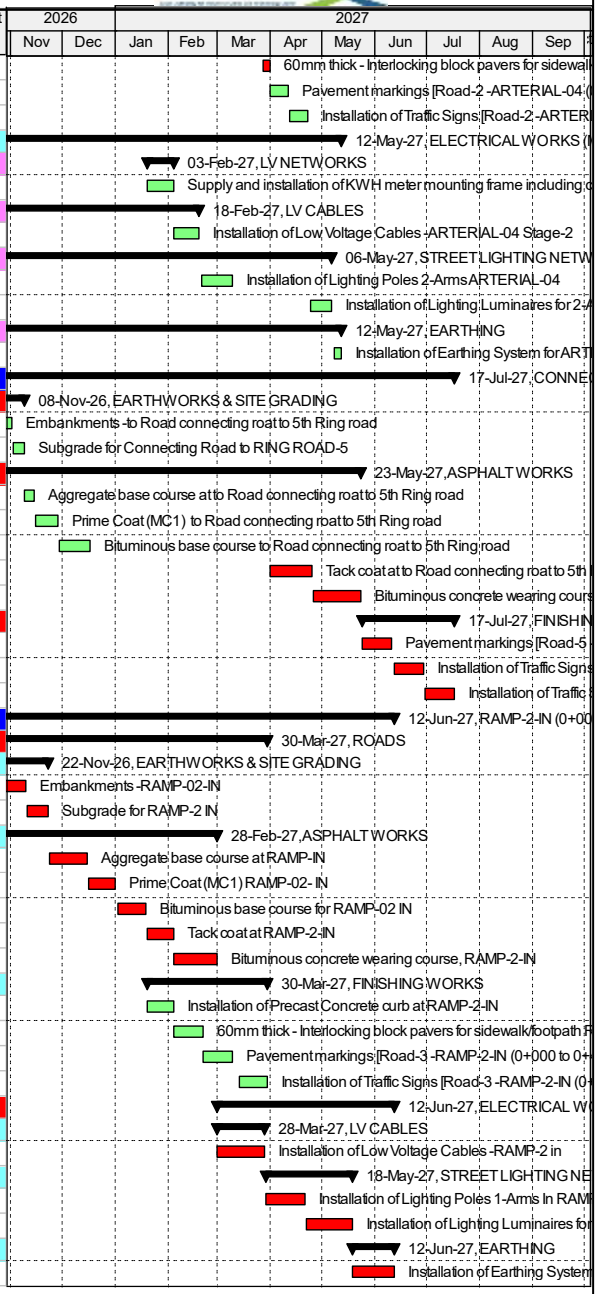

Actual Work
Remaining Work
Critical Remaining Work
Milestone


Date	Revision	Checked	Approved

egis ENJAZCO

MKH2-02-003 - Completion of Infrastructure Works at the Second Industrial City in Makkah UP 34
Remaining Work

MODON مدن

Activity ID	Activity Name	Original Duration	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Schedule % Complete	Performance % Complete	Variance - BL Project Finish Date
RAMP-2-OUT (0+398 to 0+000)		140	15-Dec-26	18-Mar-27	10-Sep-26 A	27-Apr-27	0.00	72,995.39	540,527.27	0%	13.5%	-34
ROADS		63	31-Dec-26	18-Mar-27	04-Feb-27	22-Apr-27	0.00	0.00	296,204.32	0%	0%	-30
ASPHALT WORKS		34	31-Dec-26	08-Feb-27	04-Feb-27	20-Mar-27	0.00	0.00	35,362.60	0%	0%	-30
MKH2-02-00:	Tack coat at RAMP-2-OUT	14	31-Dec-26	16-Jan-27	04-Feb-27	20-Feb-27	0.00	0.00	3,497.40	0%	0%	-30
MKH2-02-00:	Bituminous concrete wearing course	20	17-Jan-27	08-Feb-27	21-Feb-27	20-Mar-27	0.00	0.00	31,865.20	0%	0%	-30
FINISHING WORKS		49	17-Jan-27	18-Mar-27	21-Feb-27	22-Apr-27	0.00	0.00	260,841.72	0%	0%	-30
MKH2-02-00:	Installation of Precast Concrete curb	12	17-Jan-27	30-Jan-27	21-Feb-27	07-Mar-27	0.00	0.00	98,791.50	0%	0%	-30
MKH2-02-00:	60mm thick - Interlocking block pave	14	31-Jan-27	15-Feb-27	08-Mar-27	27-Mar-27	0.00	0.00	148,157.10	0%	0%	-30
MKH2-02-00:	Pavement markings [Road-4 -RAMF	11	16-Feb-27	01-Mar-27	28-Mar-27	08-Apr-27	0.00	0.00	3,642.12	0%	0%	-30
MKH2-02-00:	Installation of Traffic Signs [Road-4 -R	12	02-Mar-27	18-Mar-27	10-Apr-27	22-Apr-27	0.00	0.00	10,251.00	0%	0%	-30
ELECTRICAL WORKS (MKH2-01-007-DAR-TS8-0-S		140	15-Dec-26	18-Mar-27	10-Sep-26 A	27-Apr-27	0.00	72,995.39	244,322.95	0%	29.88%	-34
LV CABLES		21	15-Dec-26	07-Jan-27	10-Sep-26 A	21-Nov-26	0.00	24,031.79	80,105.95	0%	30%	41
MKH2-02-00:	Installation of Low Voltage Cables -R	21	15-Dec-26	07-Jan-27	10-Sep-26 A	21-Nov-26	0.00	24,031.79	80,105.95	0%	30%	41
STREET LIGHTING NETWORK INCLUDING ALL		111	09-Jan-27	01-Mar-27	10-Sep-26 A	13-Apr-27	0.00	48,963.60	163,212.00	0%	30%	-34
MKH2-02-00:	Installation of Lighting Poles 1-Arms I	19	09-Jan-27	30-Jan-27	10-Sep-26 A	13-Dec-26	0.00	37,305.60	124,352.00	0%	30%	41
MKH2-02-00:	Installation of Lighting Luminaires for	12	15-Feb-27	01-Mar-27	12-Sep-26 A	13-Apr-27	0.00	11,658.00	38,860.00	0%	30%	-34
EARTHING		12	02-Mar-27	18-Mar-27	14-Apr-27	27-Apr-27	0.00	0.00	1,005.00	0%	0%	-34
MKH2-02-00:	Installation of Earthing System for RA	12	02-Mar-27	18-Mar-27	14-Apr-27	27-Apr-27	0.00	0.00	1,005.00	0%	0%	-34
DEMOLISHING WORKS		14	23-Jun-26	08-Jul-26	28-Oct-26	12-Nov-26	33,500.00	0.00	33,500.00	100%	0%	-108
DEMOLISHING Works		14	23-Jun-26	08-Jul-26	28-Oct-26	12-Nov-26	33,500.00	0.00	33,500.00	100%	0%	-108
MKH2-02-003-(	Milling of the existing asphalt layer	14	23-Jun-26	08-Jul-26	28-Oct-26	12-Nov-26	33,500.00	0.00	33,500.00	100%	0%	-108
Open Drain Channels		177	30-Mar-27	14-Jun-27	23-Jul-26 A	06-Jul-27	0.00	509,563.69	1,470,171.32	0%	34.66%	-19
Near Ramp- In location from Ch 0+000 to Ch 0+230		177	30-Mar-27	14-Jun-27	23-Jul-26 A	06-Jul-27	0.00	509,563.69	1,470,171.32	0%	34.66%	-19
MKH2-02-003-(	Excavation for Channel	21	30-Mar-27	22-Apr-27	23-Jul-26 A	19-Jan-27	0.00	417,409.98	425,928.55	0%	98%	76
MKH2-02-003-(	Embankment for Channel Berms	21	24-Apr-27	20-May-27	09-Sep-26 A	13-Feb-27	0.00	52,528.00	53,600.00	0%	98%	76
MKH2-02-003-(	Riprap Grouting	21	22-May-27	14-Jun-27	09-Sep-26 A	06-Jul-27	0.00	39,625.71	990,642.77	0%	4%	-19
TESTING & COMMISSIONING		76	20-Mar-27	26-Jun-27	20-Oct-26 A	24-Jul-27	0.00	260,127.58	5,202,551.60	0%	5%	-24
MKH2-02-003-TC	Test for Electrical Networks	6	08-May-27	13-May-27	20-Oct-26 A	19-Jun-27	0.00	260,127.58	1,300,637.90	0%	20%	-28
MKH2-02-003-TC	Test for Box Culvert	6	20-Mar-27	25-Mar-27	24-Apr-27	29-Apr-27	0.00	0.00	1,300,637.90	0%	0%	-30
MKH2-02-003-TC	Test for Open Drain channel	10	15-Jun-27	26-Jun-27	07-Jul-27	18-Jul-27	0.00	0.00	1,300,637.90	0%	0%	-19
MKH2-02-003-TC	Test for Roads	6	08-Jun-27	14-Jun-27	18-Jul-27	24-Jul-27	0.00	0.00	1,300,637.90	0%	0%	-34
PROJECT CLOSEOUT & DEMOBILIZA		107	27-Mar-27	14-Aug-27	01-May-27	05-Sep-27	0.00	0.00	0.00	0%	0%	-19
As-Built DWGs		85	27-Mar-27	19-Jul-27	01-May-27	10-Aug-27	0.00	0.00	0.00	0%	0%	-19
As-Built DWGs Submittals		77	27-Mar-27	07-Jul-27	01-May-27	01-Aug-27	0.00	0.00	0.00	0%	0%	-21
MKH2-02-003-(	As-Built DWGs Submittal for Electrica	7	18-May-27	25-May-27	20-Jun-27	27-Jun-27	0.00	0.00	0.00	0%	0%	-28
MKH2-02-003-(	As-Built DWGs Submittal for Box Cu	7	27-Mar-27	03-Apr-27	01-May-27	08-May-27	0.00	0.00	0.00	0%	0%	-30
MKH2-02-003-(	As-Built DWGs Submittal for Open D	10	27-Jun-27	07-Jul-27	19-Jul-27	29-Jul-27	0.00	0.00	0.00	0%	0%	-19
MKH2-02-003-(	As-Built DWGs Submittal for Roads	7	15-Jun-27	22-Jun-27	25-Jul-27	01-Aug-27	0.00	0.00	0.00	0%	0%	-34
As-Built DWGs Approvals		78	04-Apr-27	19-Jul-27	09-May-27	10-Aug-27	0.00	0.00	0.00	0%	0%	-19
MKH2-02-003-(	As-Built DWGs Approval for Electrica	9	26-May-27	05-Jun-27	28-Jun-27	07-Jul-27	0.00	0.00	0.00	0%	0%	-28
MKH2-02-003-(	As-Built DWGs Approval for Box Cul	7	04-Apr-27	11-Apr-27	09-May-27	19-May-27	0.00	0.00	0.00	0%	0%	-30
MKH2-02-003-(	As-Built DWGs Approval for Open D	10	08-Jul-27	19-Jul-27	31-Jul-27	10-Aug-27	0.00	0.00	0.00	0%	0%	-19
MKH2-02-003-(	As-Built DWGs Approval for Roads	7	23-Jun-27	30-Jun-27	02-Aug-27	09-Aug-27	0.00	0.00	0.00	0%	0%	-34
Demobilization		22	20-Jul-27	14-Aug-27	11-Aug-27	05-Sep-27	0.00	0.00	0.00	0%	0%	-19
MKH2-02-003-C	Demobilization of Manpower	5	20-Jul-27	25-Jul-27	11-Aug-27	16-Aug-27	0.00	0.00	0.00	0%	0%	-19
MKH2-02-003-C	Removal of Equipment from Site	5	26-Jul-27	31-Jul-27	17-Aug-27	22-Aug-27	0.00	0.00	0.00	0%	0%	-19
MKH2-02-003-C	Site Clean Up	5	01-Aug-27	05-Aug-27	23-Aug-27	28-Aug-27	0.00	0.00	0.00	0%	0%	-19
MKH2-02-003-C	Restoration of Ground Surfaces	7	07-Aug-27	14-Aug-27	29-Aug-27	05-Sep-27	0.00	0.00	0.00	0%	0%	-19

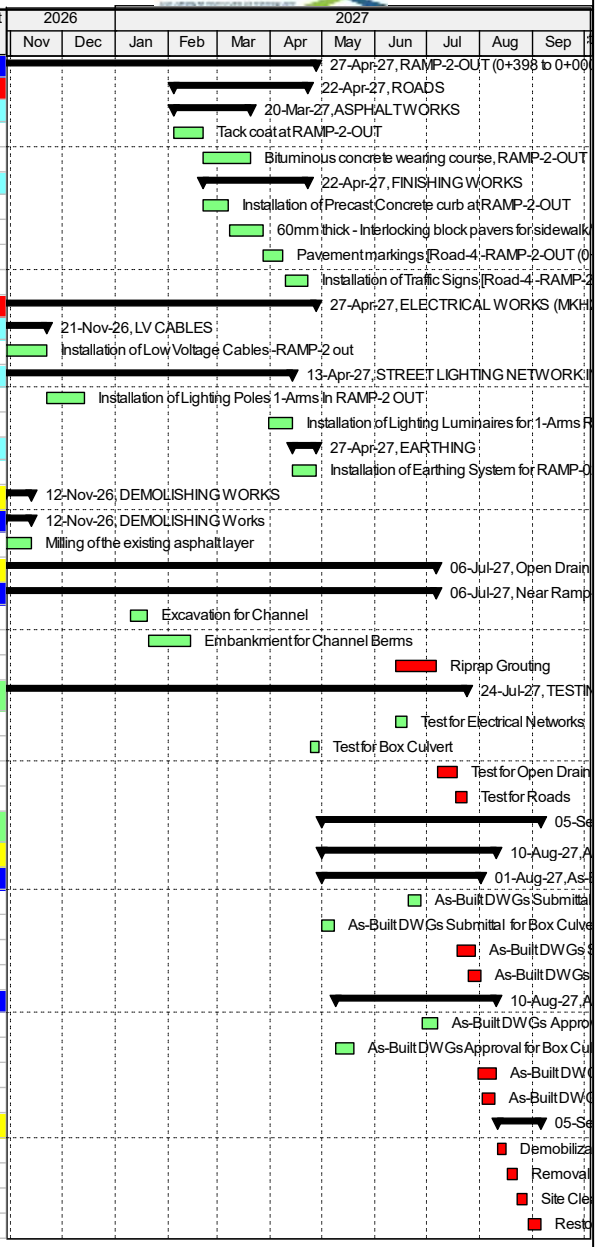

Actual Work
Remaining Work
Critical Remaining Work
Milestone

Date	Revision	Checked	Approved
