Playground Initiative for Eastern Region (Arar, Hasa Oasis, Dammam 2nd)

مبادرة الملاعب بالمنطقة الشرقية (عرعر, واحة الاحساء, الدمام الثانية)

CLIENT	CONTRACTOR	CONSULTANT	MODON PM	SITE HANDOVER	CONTRACT COMPLETION
MODON	Profast Company Ltd.	EGIS	Eng. Mohamed Alisa	03-Mar-2026	02-Jan-2027

Scope: football, basketball and padel grounds, an air dome, a service and toilet building, landscape works, parking, and bike and walking paths at three sites: Hasa Oasis, the 2nd Industrial City at Arar and the 2nd Industrial City at Dammam.

Status at a glance

Progress is measured as physical % complete, weighted by budgeted man-hours. The project is at 53.9% against 53.7% planned, 0.2% ahead of the current plan (SPI 1.00). It gained 3.6% this week against 3.6% planned. Hasa Oasis construction is ahead (61.4% against 44.9% planned), while Arar is 1.9% behind and procurement is 28.6% behind.

PHYSICAL % COMPLETE

53.9% / 53.7% plan

▲ SPI 1.00 +0.2%

PROGRESS THIS WEEK

+3.6% / +3.6% plan

● In line with the weekly plan

CONTRACT TIME ELAPSED

77.7% · day 237 of 305

▼ Forecast finish 14-Mar-2027

INVOICED TO DATE (GROSS)

15.0% · 4.50M SAR


6 invoices, last period ends 20-Oct-2026

Project completion is forecast 71 days late.

The weekly report and the P6 update (data date 26-Oct-2026) both forecast completion on 14-Mar-2027, against the contract completion date of 02-Jan-2027. P6 shows −57 days of float on project completion and 268 open activities with negative float. All three site-completion milestones are forecast for 28-Feb to 01-Mar-2027. Supply of the air dome is the cause of delay named in the weekly summary. Against the original baseline, which called for 85.7% by the end of October, the project is at 53.9%.

Progress S-curve

Cumulative physical progress (man-hour weighted), month-end values; the October actual is at the 26-Oct data date. Source: Physical-Chart Data sheet, weekly report 26-Oct-2026.

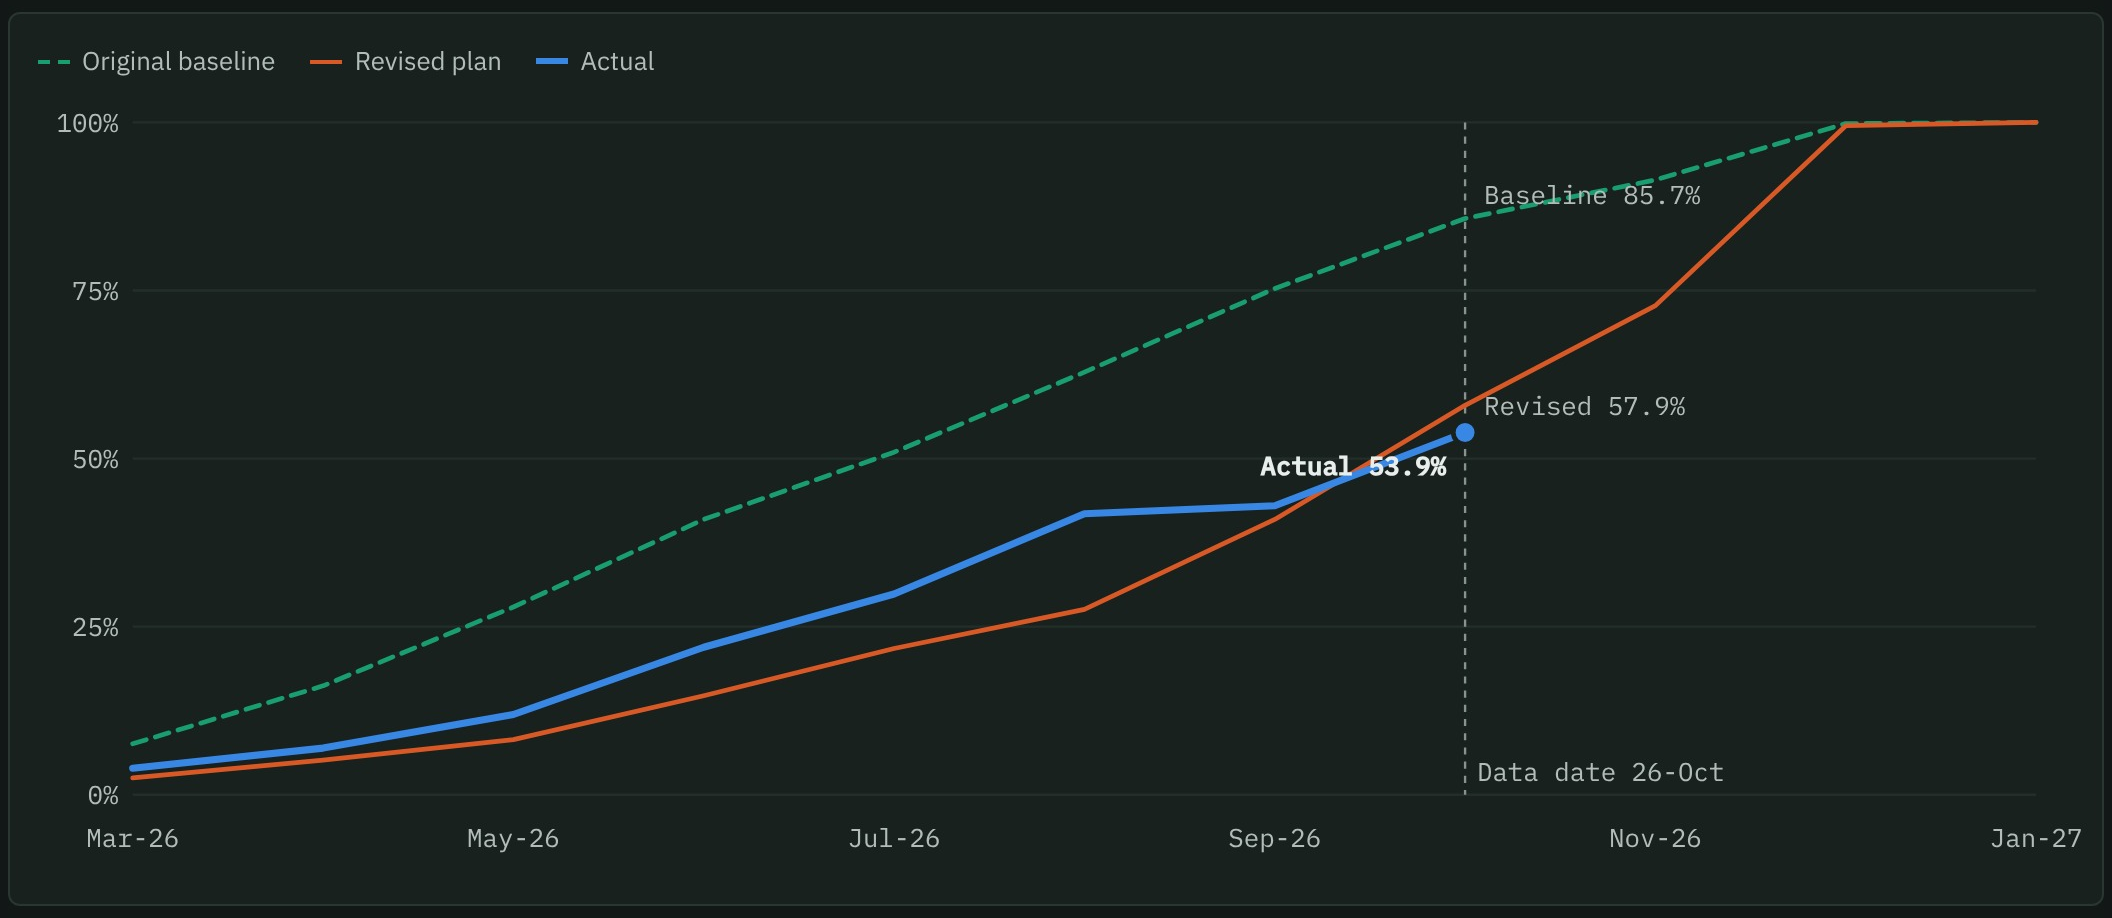

WEEK ENDING	PLANNED %	ACTUAL %	VARIANCE	GAINED THIS WEEK	SPI
28-Sep-2026	–	43.0	–	–	–
05-Oct-2026	–	46.0	–	+3.0	–
12-Oct-2026	–	46.9	–	+0.9	–
19-Oct-2026	50.1	50.3	+0.2	+3.4	1.00
26-Oct-2026	**53.7**	**53.9**	**+0.2**	**+3.6**	**1.00**

Actual values are the weekly points of the Physical-Chart Data sheet, one per Monday data date. Planned values for 19 and 26 Oct come from the P6 extracts in the Progress sheet; the sheet gives no weekly plan for earlier weeks. No earlier weekly report for this project has been uploaded.

Progress by phase


Physical progress to date by WBS, weighted by budgeted man-hours. Source: Weekly Progress Report sheet, 26-Oct-2026.

PHASE	WEIGHT	PLANNED	ACTUAL	VARIANCE	SPI	STATUS
Mobilization	3.0%	100.0%	100.0%	0.0%	1.00	✓ Complete
Engineering	5.0%	97.3%	99.5%	+2.3%	1.02	▲ Ahead
Procurement	12.0%	80.3%	51.7%	−28.6%	0.64	▼ Behind
Construction	75.0%	48.2%	52.9%	+4.7%	1.10	▲ Ahead
Construction: Arar	24.9%	47.1%	45.2%	−1.9%	0.96	▼ Slightly behind
Construction: Hasa Oasis	25.0%	44.9%	61.4%	+16.6%	1.37	▲ Ahead
Construction: Dammam	25.0%	52.7%	52.1%	−0.6%	0.99	● On plan
Testing & commissioning	3.0%	0.0%	0.0%	0.0%	–	○ Not started
Close-out	2.0%	0.0%	0.0%	0.0%	–	○ Not started
Total	100%	**53.7%**	**53.9%**	**+0.2%**	**1.00**	● On plan

By site, all phases included: Arar 50.5% against 54.1% planned, Hasa Oasis 61.0% against 53.0%, Dammam 53.4% against 57.1%. The P6 update has 2,150 activities: 1,818 completed, 26 in progress and 306 not started. Its scheduled finish is 14-Mar-2027, 71 days after the contract date.

Scope of work: quantities

Total quantity and quantity executed to date for the main BOQ items, all three sites combined, from the Major Quantities sheet of the 26-Oct-2026 weekly report. The sheet does not split quantities by site. No earlier report has been uploaded, so the this-week column is empty.

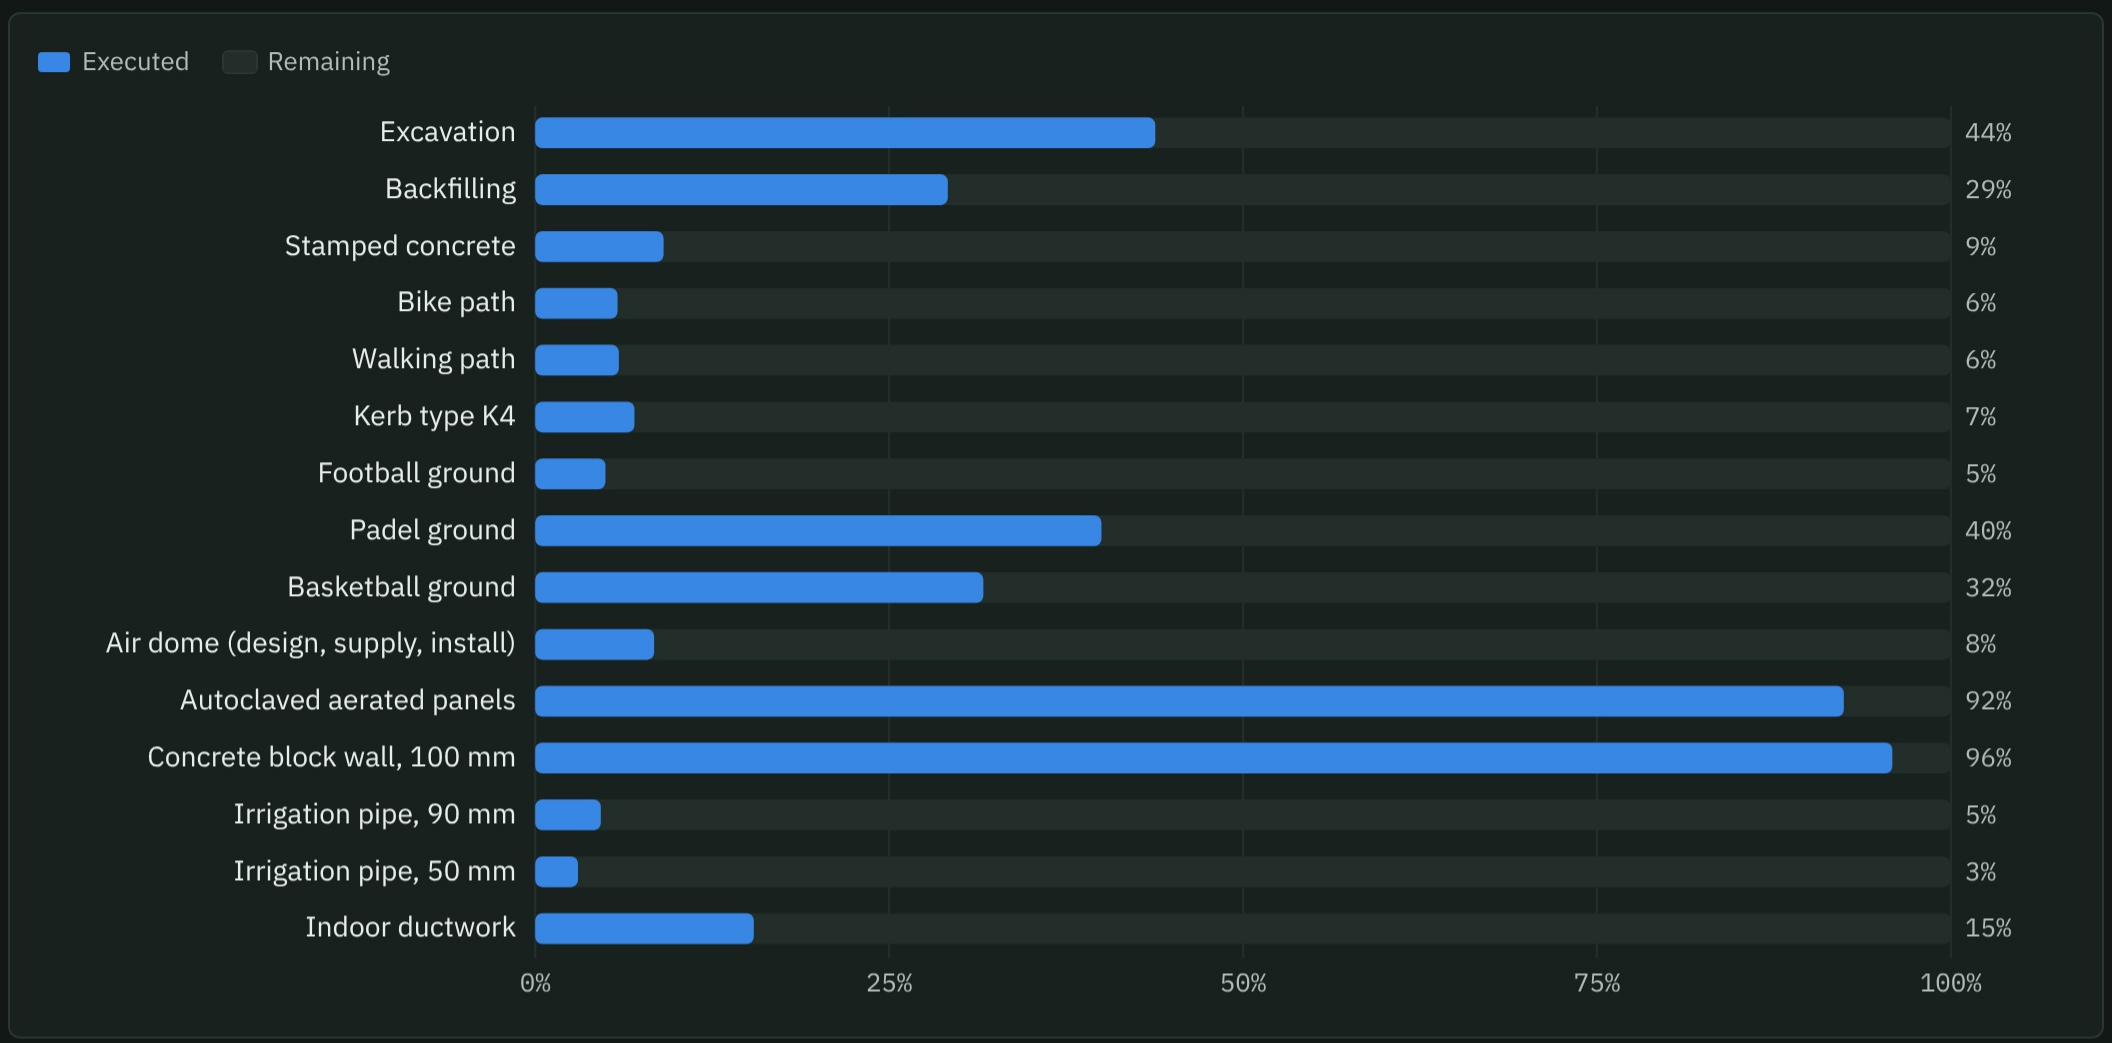

SCOPE ITEM	ZONE	UNIT	TOTAL	FINISHED	THIS WEEK	REMAINING	% FINISHED	BACKFILLED
Excavation	All sites	m³	10,295	4,510	–	5,785	43.8%	–
Backfilling	All sites	m³	10,266	2,992	–	7,274	29.1%	–
Stamped concrete	All sites	m²	1,800	163.3	–	1,637	9.1%	–
Bike path	All sites	m²	2,300	133.8	–	2,166	5.8%	–
Walking path	All sites	m²	2,200	130.1	–	2,070	5.9%	–
Kerb type K4	All sites	LM	9,080	636.7	–	8,443	7.0%	–
Football ground	All sites	m²	3,000	148.9	–	2,851	5.0%	–
Padel ground	All sites	m²	600	240	–	360	40.0%	–
Basketball ground	All sites	m²	1,530	484.4	–	1,046	31.7%	–
Air dome (design, supply, install)	All sites	item	3	0.3	–	2.7	8.4%	–
Autoclaved aerated panels	All sites	m²	750	693.3	–	56.7	92.4%	–
Concrete block wall, 100 mm	All sites	m²	135	129.4	–	5.6	95.9%	–
Irrigation pipe, 90 mm	All sites	LM	750	34.8	–	715.2	4.6%	–
Irrigation pipe, 50 mm	All sites	LM	350	10.6	–	339.4	3.0%	–
Indoor ductwork	All sites	kg	300	46.3	–	253.7	15.4%	–

Status by site this week

Hasa Oasis: asphalt layer on the football ground finished, interlock being laid between the grounds, lighting poles and fittings installed, planting under way. Dammam: interlock compaction on all three grounds, sewer line finished and being backfilled, lighting fittings being installed. Arar: floor ceramics finished, gypsum board and painting in the service building, lighting cables laid and backfilled. Air dome entrance foundations are being formed at Arar and Dammam.

Items above the BOQ quantity

Several items are reported beyond their BOQ total: 150 mm uPVC external wastewater pipe (126.81 of 50 m), plastering (551.07 of 471 m²), foundation waterproofing membrane (101.55 of 60 m²), slab on grade (46.17 of 45 m³) and polyethylene sheet and anti-termite (288.75 of 270 m²). They are left out of the chart and table.

Milestones

The weekly report's Milestones sheet and the P6 update give the same forecast dates. Float is from the P6 update (data date 26-Oct-2026).

MILESTONE	BASELINE	WEEKLY REPORT FORECAST	P6 UPDATE FORECAST	P6 FLOAT (DAYS)	STATUS
Project commencement	03-Mar-2026	03-Mar-2026	03-Mar-2026 (actual)	–	✓ Done
Baseline programme approval	01-Apr-2026	04-Apr-2026	04-Apr-2026 (actual)	–	✓ Done
Completion of mobilization	02-Apr-2026	02-Apr-2026	02-Apr-2026 (actual)	–	✓ Done
Completion of levelling works	02-Apr-2026	02-May-2026	02-May-2026 (actual)	–	✓ Done
Completion of engineering	02-May-2026	27-Dec-2026	27-Dec-2026	+1	▼ Late
Completion of toilet building	02-Aug-2026	01-Mar-2027	01-Mar-2027	−50	▼ Late
Completion of playground area	24-Aug-2026	01-Mar-2027	01-Mar-2027	−50	▼ Late
Completion of natural landscape works	02-Nov-2026	01-Mar-2027	01-Mar-2027	−49	▼ Late
Completion of Arar works	21-Dec-2026	01-Mar-2027	01-Mar-2027	−49	▼ Late
Completion of Hasa Oasis works	21-Dec-2026	01-Mar-2027	01-Mar-2027	−49	▼ Late
Completion of Dammam works	21-Dec-2026	28-Feb-2027	28-Feb-2027	−48	▼ Late
Completion of testing & commissioning	21-Dec-2026	09-Mar-2027	09-Mar-2027	−56	▼ Late
Project completion	02-Jan-2027	14-Mar-2027	14-Mar-2027	−57	▼ Late

The air dome and the late electrical and finishing packages drive the finish date.

In P6 the PVC membrane deliveries run from 27-Oct to 17-Dec-2026 and membrane installation from 23-Dec-2026 to 14-Jan-2027, with −5 to −31 days of float. The most negative float (−57 days) sits on air dome control systems and signs, switches and sockets, power outlets, CCTV and MEP testing for the playground area. Testing and commissioning of all three areas is forecast for 20-Feb to 28-Feb-2027.

Procurement of key materials

Share of total quantity delivered to site. Source: supply tracking file (ملف التوريدات), 26-Oct-2026.



The weekly report's procurement summary counts 119 materials: 116 purchase orders issued, 3 still to issue, 99 materials on site and 20 still to arrive.

Air dome: nothing delivered yet


Purchase orders are issued and advance payments made for the membrane, anchors, L-profiles, lighting, ventilation, generators, ATS, doors, fire-fighting, panels and electrical material, with supply scheduled from 01-Nov to 05-Dec-2026. The 18 package units are still in final approval, the anchor sample awaits approval, door samples are being resubmitted, and the entrance steel and curtain wall are being manufactured.

Landscape, path and ground surfaces

Trees (298), lawn (7,030 m²), tartan floor (510 m²), bike and walking path surfaces (4,281 m²) and the football and padel ground surfaces are ordered and paid, with supply due between 29-Oct and 30-Nov-2026. The path and ground finishing layer is tied to the air dome finishing. Lighting fixtures (105) are paid and ready to supply; LV panel boards (9) are being manufactured.

Manpower

Monthly head count on site (manual and non-manual), planned vs actual. Source: Manpower sheet.

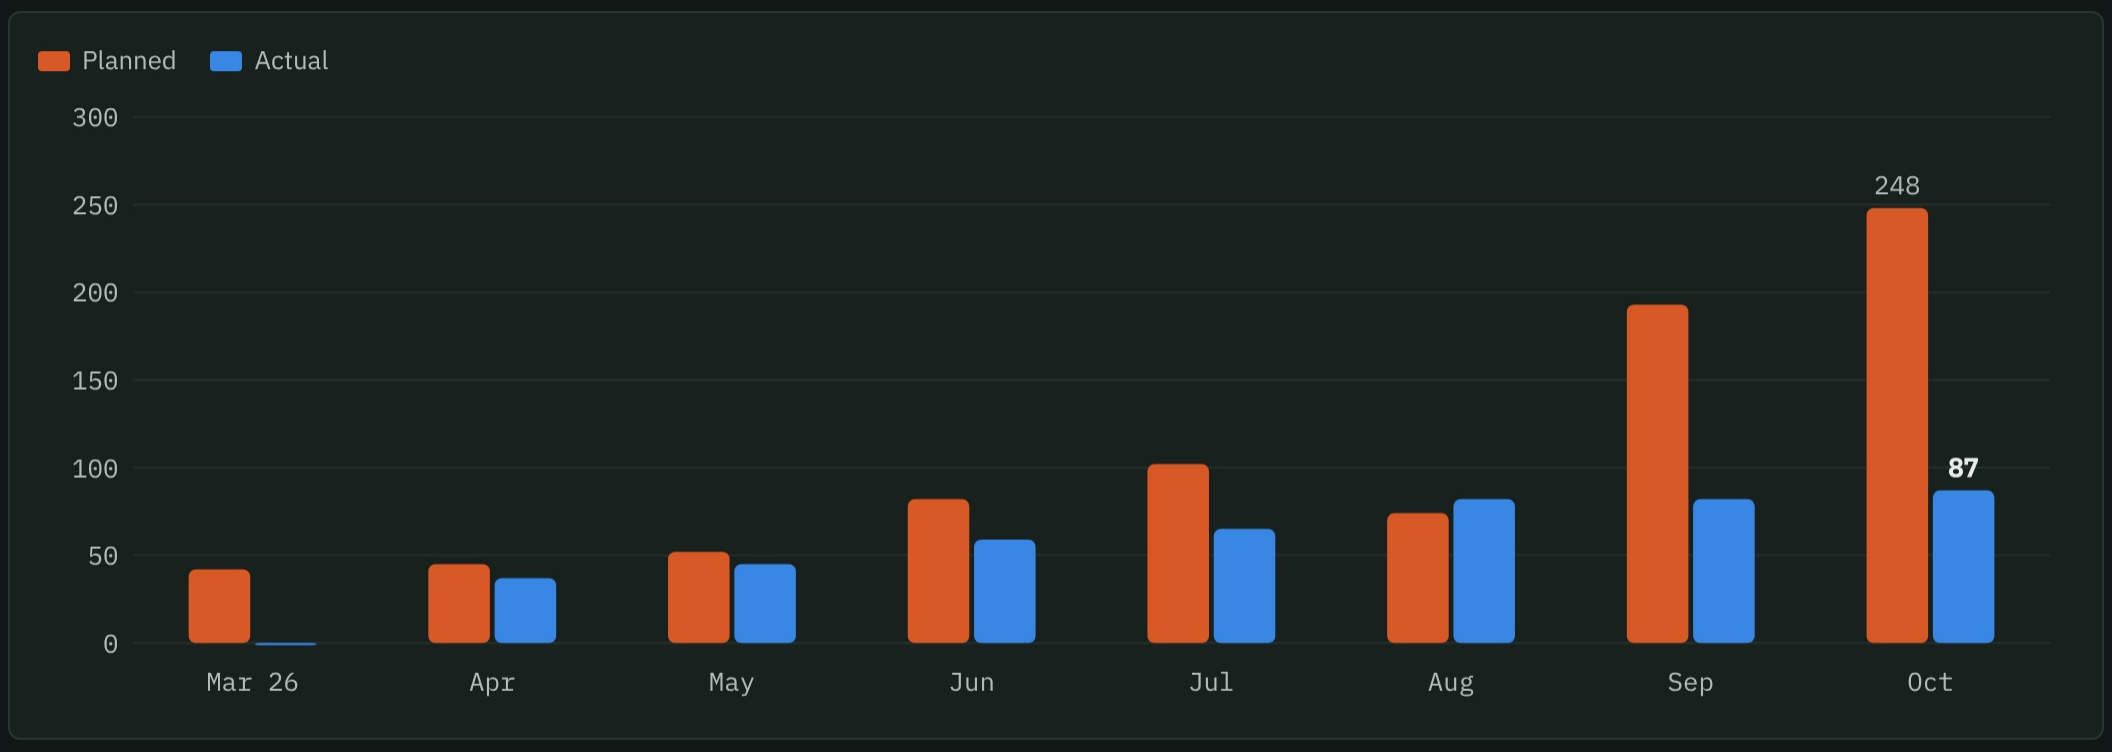

October head count is 87 against 248 planned (−65%): 68 workers against 229 planned and 19 staff as planned. Equipment on site is 12 against 37 planned. The plan rises to 380 in December 2026.

Cost and invoicing

Contract value

Playground works	20,775,269
Site works	5,722,500
Service buildings	3,500,083
Contract value (excl. VAT)	**29,997,852**
Contract value incl. 15% VAT	34,497,529
Change orders	0

All values in SAR, from the Progress Summary and Invoice Log sheets. No change orders are registered.

Invoices

Invoices submitted	6
Gross value	4,501,527
Approved by MODON PM (5 invoices)	3,673,916
Paid (3 invoices)	2,178,751
Deductions and penalties	59,000
Net incl. VAT	5,117,756
FIR value to date	5,381,841

Invoicing is 15.0% of the contract value against 53.9% physical progress, and approved field inspections are worth 17.9%. No advance payment or retention is recorded.

Health, safety and quality

Safety Score 0.89

Safe man-hours (cumulative)	44,620
Man-hours this week	1,450
Lost-time injuries	0
Fatalities	0
First-aid cases	0
Near misses	0
Inductions / toolbox talks	32 / 107
Internal audits	5

Quality Score 0.86

FIRs issued / closed / pending	952 / 914 / 38
MIRs issued / closed / pending	184 / 167 / 17
NCRs issued / closed / pending	29 / 27 / 2
Site instructions issued / closed / pending	14 / 6 / 8
Shop drawing submittals (134 planned)	159
Material submittals (119 planned)	140

Cumulative counts from the Quality-Stat sheet. All pending items are less than 10 days old.

Open issues and risks

ISSUE	OWNER	DETAIL
Air dome supply	Contractor	Late manufacture and supply of the air dome is the cause of delay named in the weekly summary. The risk register rates late delivery of this long-lead item as high likelihood and very high impact. Membrane delivery and installation run with negative float.
Shop drawing submittals	Contractor	Open since 03-Apr-2026, expected to close on 29-Oct-2026. Two shop drawings remain to be submitted.
Procurement behind plan	Contractor	Procurement is at 51.7% against 80.3% planned (physical). Twenty materials are not yet on site and three purchase orders are still to be issued.
Manpower and equipment	Contractor	68 workers on site in October against 229 planned, and 12 pieces of equipment against 37 planned, while the plan calls for 361 workers in December.
Interfaces between finishes and the air dome	Contractor	The supply file ties the final layer of the paths and grounds to the air dome finishing, to avoid damage; these surfaces are 60% paid but not delivered.

Closed this week: the level difference at the Al-Ahsa site and the Al-Ahsa septic tank missing from the payment certificate. Other open risks in the register cover site access, confined spaces, material storage, equipment certification, work at height, heat and traffic separation.

Data notes

- Week number: the Milestones sheet states "Current Contract Weeks: 26 of 44", which is the report number (WPR-26) and does not match the dates. From site handover on 03-Mar-2026 to the 26-Oct-2026 data date is 237 days, which is week 33; this report uses 33. The Weekly Progress Report and HSE sheets give the report number as 25.
- The report's weekly physical progress (20,555 man-hours, 4.91%) is the change between its two P6 extracts (231,540 man-hours on 26-Oct and 210,985 on 19-Oct). Its to-date figure is 225,576 man-hours (53.9%), not the 231,540 (55.3%) in the 26-Oct extract; the gap is in the procurement man-hours for Hasa Oasis (7,939 vs 10,266) and Dammam (7,414 vs 11,116). This report uses 53.9% and the Physical-Chart Data series, which gives +3.6% this week.
- The MODON summary files (Look Ahead, الأعمال المنفذة ونسب الإنجاز, الأعمال المنفذه خلال الإسبوع) and the Progress Summary sheet label cost-based progress as actual progress. Those figures are not used here.
- The file الأعمال المنفذه خلال الإسبوع carries details of another project: project manager عبد الله الشنيفي, contractor شركة الانجاز, start 24-Nov-2025, contract end 23-May-2026 and sector القطاع الأوسط. The Look Ahead file lists the consultant EGIS in the contractor column.
- The milestone table on the Weekly Progress Report sheet has its names shifted by one row against the Milestones sheet, for example "Completion of Toilet Building" with the levelling-works dates. Completion of engineering is marked actual although P6 forecasts 27-Dec-2026, and the Tracking Progress file shows the toilet building milestone at 100% while P6 has it not started.
- No site photos could be used: the six photos in the weekly report's Weekly Photos sheet are embedded at 414 × 311 px, below the 600 px minimum, and no separate photo files were uploaded.
- Major Quantities: several items exceed their BOQ quantity (see Scope of work), "Plan To Date" equals the full quantity for every item, and some rows show #DIV/0!. The executed quantities look low against the narrative (for example 636.74 LM of K4 kerb, while the supply file reports 6,448 LM of curbstone installed); please confirm the measurement basis.
- The Failed Start List file is dated 19-10-2026 in its name, the previous week. Several summary cells in the DB and Invoice Log sheets show #REF! errors.
- Equipment on site is 10 in one table of the Manpower sheet and 12 in another. Two safety audit closure dates in the HSE-Stat sheet read 2006.
- The split of the contract value by site differs between the Weekly Progress Report sheet (Arar 10,110,715) and the P6 extract in the Progress sheet (Arar 10,226,640).

Compiled 01-Nov-2026 from the weekly report with data date 26-Oct-2026 (WPR-26).
