Infrastructure Networks for the 1 km² Logistics Zone, 2nd Industrial City, Dammam

شبكات البنية التحتية للمنطقة اللوجستية لمساحة 1 كم مربع بالمدينة الصناعية الثانية بالدمام

CLIENT	CONTRACTOR	CONSULTANT	MODON PM	SITE HANDOVER	CONTRACT COMPLETION
MODON	Shibh Aljazira Contracting Company	Egis	Muhammad H Al-Essa	30-Jul-2025	29-Jan-2027

Scope: phase 1 of the logistics area. Wet networks (sewerage, storm, potable water, fire fighting and TSE, including the force main), dry networks (medium voltage, low voltage, street lighting and telecom), the potable water pump station, the sewage lift station, guard rooms, all road layers up to the asphalt wearing course, and landscape.

Status at a glance

Progress is measured as physical % complete, weighted by budgeted man-hours. At the 03-Nov-2026 data date the project is 62.1% complete against 80.1% planned, 18.0% behind the plan (SPI 0.78). It gained 1.4% this week against 4.1% planned, so the gap widened from 15.3% to 18.0%.

PHYSICAL % COMPLETE

62.1% / 80.1% plan

▼ SPI 0.78 −18.0%

PROGRESS THIS WEEK

+1.4% / +4.1% plan

▼ 2.7% below the weekly plan

CONTRACT TIME ELAPSED

84.1% · day 461 of 548

▼ Forecast handover 15-Mar-2027

INVOICED TO DATE (GROSS)

31.6% · 62.9M SAR

7 invoices, last period ends 15-Sep-2026

With 84.1% of the contract time gone, 37.9% of the work remains.

Finishing by the contract completion date of 29-Jan-2027 needs about 3.2% a week over the 12 whole weeks left, against 1.4% achieved this week. The weekly report's milestone sheet and the P6 update now forecast project handover on 15-Mar-2027, 45 days late, a week later again than last week's forecast. Construction is the weak phase: 52.5% done against 84.3% planned.


Site photos this week

Six site photos from the 03-Nov-2026 progress presentation; this week's upload has no separate photo files. Camera stamps run from 31 Oct to 02 Nov 2026 where visible. Select a photo to view it larger, then use the arrows to move between photos.



Prime coat spraying, Road 2

MC1 prime coat on the base course. Camera-stamped 02-Nov-2026, 08:45, Dhahran.

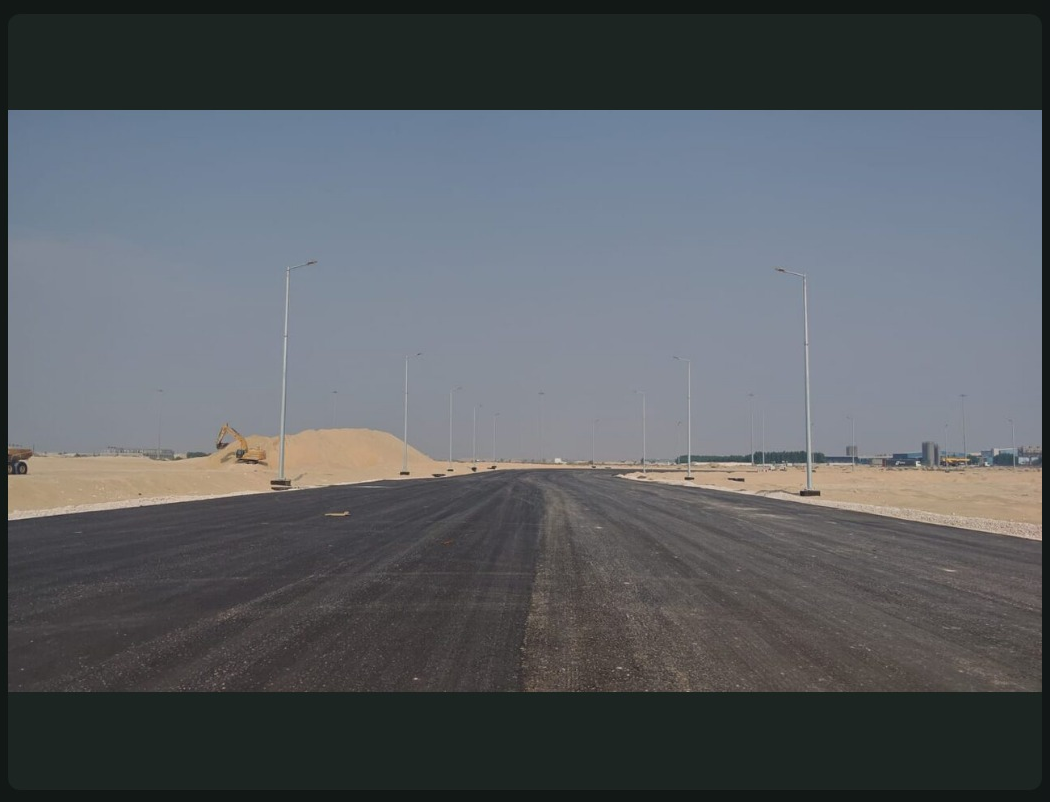

Asphalt and street lighting, Road 2 Zone 4

Asphalt laid with lighting poles installed. No date stamp.




Box culvert waterproofing

Waterproofing on the culvert wall. Camera-stamped 01-Nov-2026, 09:15.




Tank reinforcement

Steel fixing for the tank walls. No date stamp.

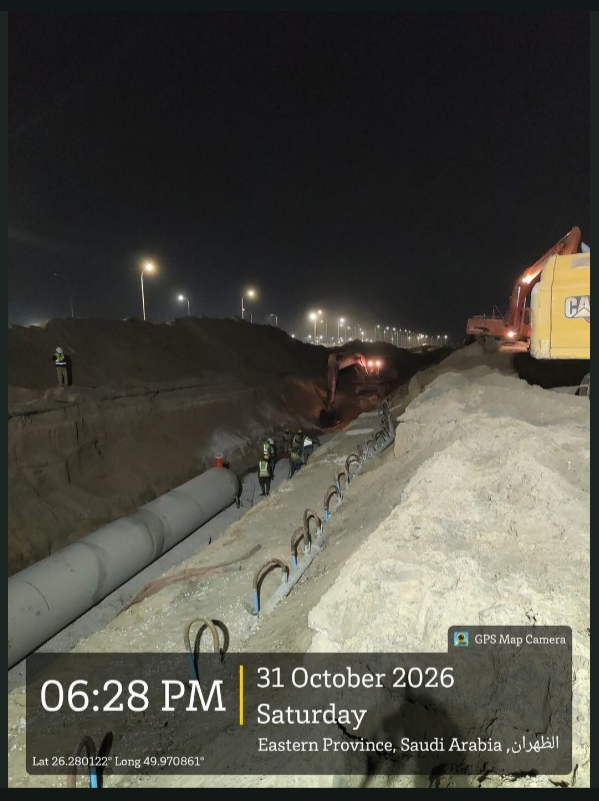

Pipe laying at night

Camera-stamped 31-Oct-2026, 18:28, GPS 26.280122° N, 49.970861° E.

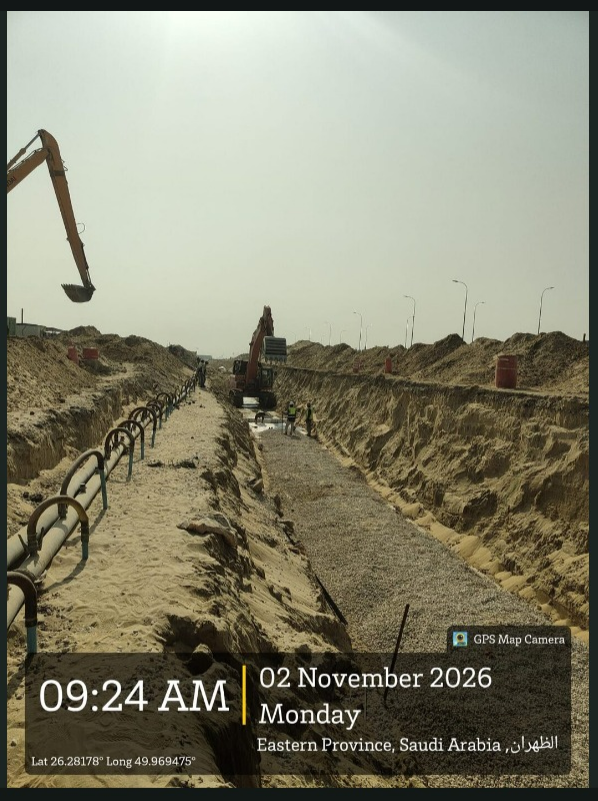


Trench with bedding

Camera-stamped 02-Nov-2026, 09:24, GPS 26.28178° N, 49.969475° E.

Progress S-curve

Cumulative physical progress (man-hour weighted), month-end values. Source: Physical-Chart Data sheet. The November actual is the 03-Nov value.

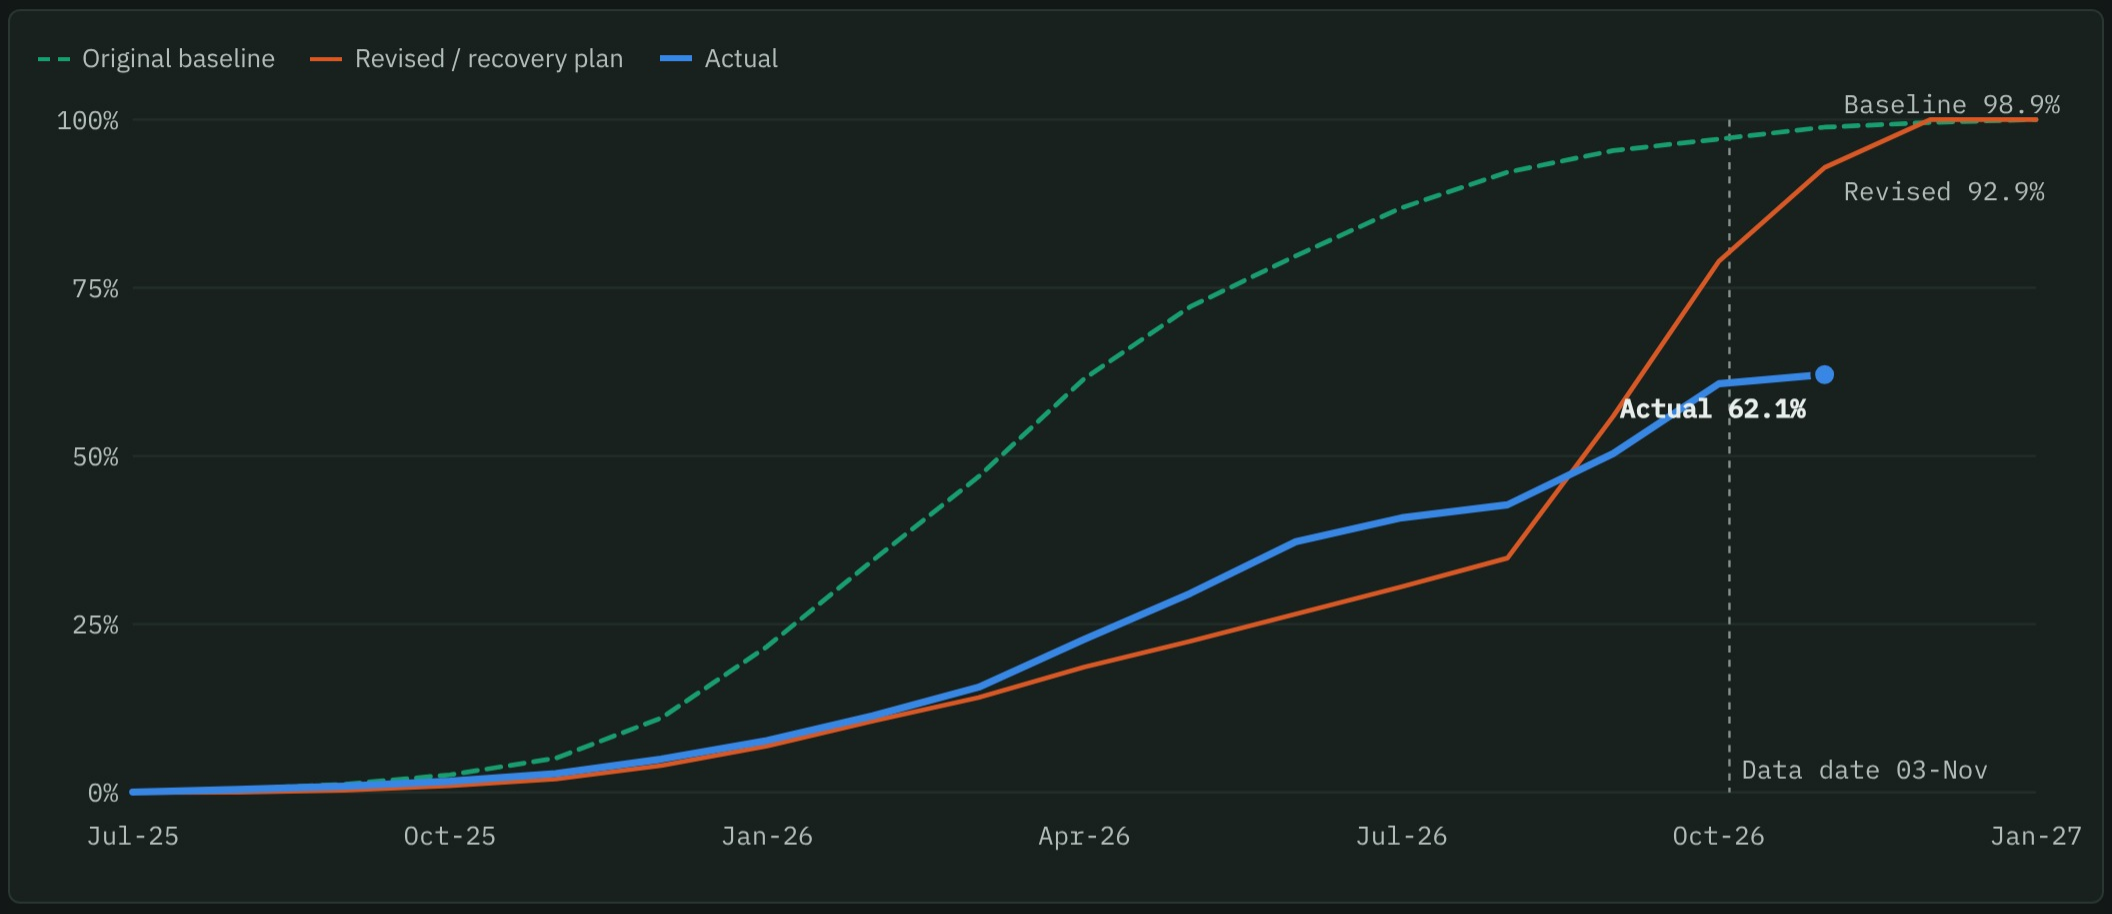

WEEK ENDING	PLANNED %	ACTUAL %	VARIANCE	GAINED THIS WEEK	SPI
20-Oct-2026	71.1	57.9	−13.2	+2.1	0.81
27-Oct-2026	76.0	60.7	−15.3	+2.8	0.80
03-Nov-2026	**80.1**	**62.1**	**−18.0**	**+1.4**	**0.78**

Weekly values from the 20-Oct, 27-Oct and 03-Nov weekly reports. This week's report restates earlier monthly actuals again, this time upwards (September 2026: 50.3%, previously 48.9%). The contractor's forecast reaches 79.4% by the end of December, 99.9% in January and 100% in February 2027.

Progress by phase

Physical progress to date by phase, weighted by budgeted man-hours, summed over all networks from the Progress sheet.


PHASE	WEIGHT	PLANNED	ACTUAL	VARIANCE	SPI	STATUS
Demolition & earthworks	2.9%	100.0%	96.7%	-3.3	0.97	▼ Slightly behind
Engineering	3.0%	100.0%	97.3%	-2.7	0.97	▼ Slightly behind
Procurement	27.0%	96.5%	92.7%	-3.8	0.96	▼ Slightly behind
Construction	57.1%	84.3%	52.5%	-31.9	0.62	▼ Behind
Testing & commissioning	10.0%	0.0%	14.1%	+14.1	–	▲ Started early
Total	100%	**80.1%**	**62.1%**	**-18.0**	**0.78**	▼ Behind

NETWORK / WORK PACKAGE	WEIGHT	PLANNED	ACTUAL	VARIANCE	SPI	STATUS
Demolition & site clearing	0.4%	100.0%	100.0%	0.0	1.00	✓ Complete
Earthworks & site grading	2.5%	100.0%	96.2%	-3.8	0.96	▼ Slightly behind
Sewerage network	8.1%	86.6%	85.9%	-0.7	0.99	▼ Slightly behind
Storm water network	15.6%	91.1%	87.5%	-3.6	0.96	▼ Slightly behind
Potable water network	6.3%	82.1%	65.4%	-16.6	0.80	▼ Behind
Fire fighting network	6.9%	77.8%	62.4%	-15.4	0.80	▼ Behind
TSE network	5.2%	71.5%	45.2%	-26.3	0.63	▼ Behind
Potable water pump station	7.8%	83.9%	68.0%	-15.9	0.81	▼ Behind
Sewage lift station	7.7%	88.2%	70.3%	-17.9	0.80	▼ Behind
Medium-voltage network	3.7%	76.5%	48.4%	-28.1	0.63	▼ Behind
Low-voltage network	3.4%	75.1%	35.5%	-39.7	0.47	▼ Behind
Street lighting network	8.3%	61.9%	41.0%	-20.9	0.66	▼ Behind
Telecom network	6.8%	73.5%	49.5%	-24.0	0.67	▼ Behind
Road works	8.7%	81.5%	35.1%	-46.4	0.43	▼ Behind
Landscape	4.9%	46.5%	31.6%	-14.9	0.68	▼ Behind
Guard rooms	3.7%	94.3%	77.1%	-17.1	0.82	▼ Behind
Total	100%	**80.1%**	**62.1%**	**-18.0**	**0.78**	▼ Behind

Weights are budgeted man-hours. This week no man-hours were earned on the sewerage, TSE and LV networks, the pump station or landscape. The P6 update (data date 03-Nov-2026) has 4,851 activities: 2,700 completed, 496 in progress and 1,655 not started. Failed-start activities rose from 1,092 to 1,125.

Scope of work: quantities

Total, finished and remaining quantity for the main items, from the Major Quantities sheet of the 03-Nov-2026 weekly report. The sheet gives whole-site totals only, with no zones and no backfill figures. "This week" is the change since the 27-Oct-2026 report.

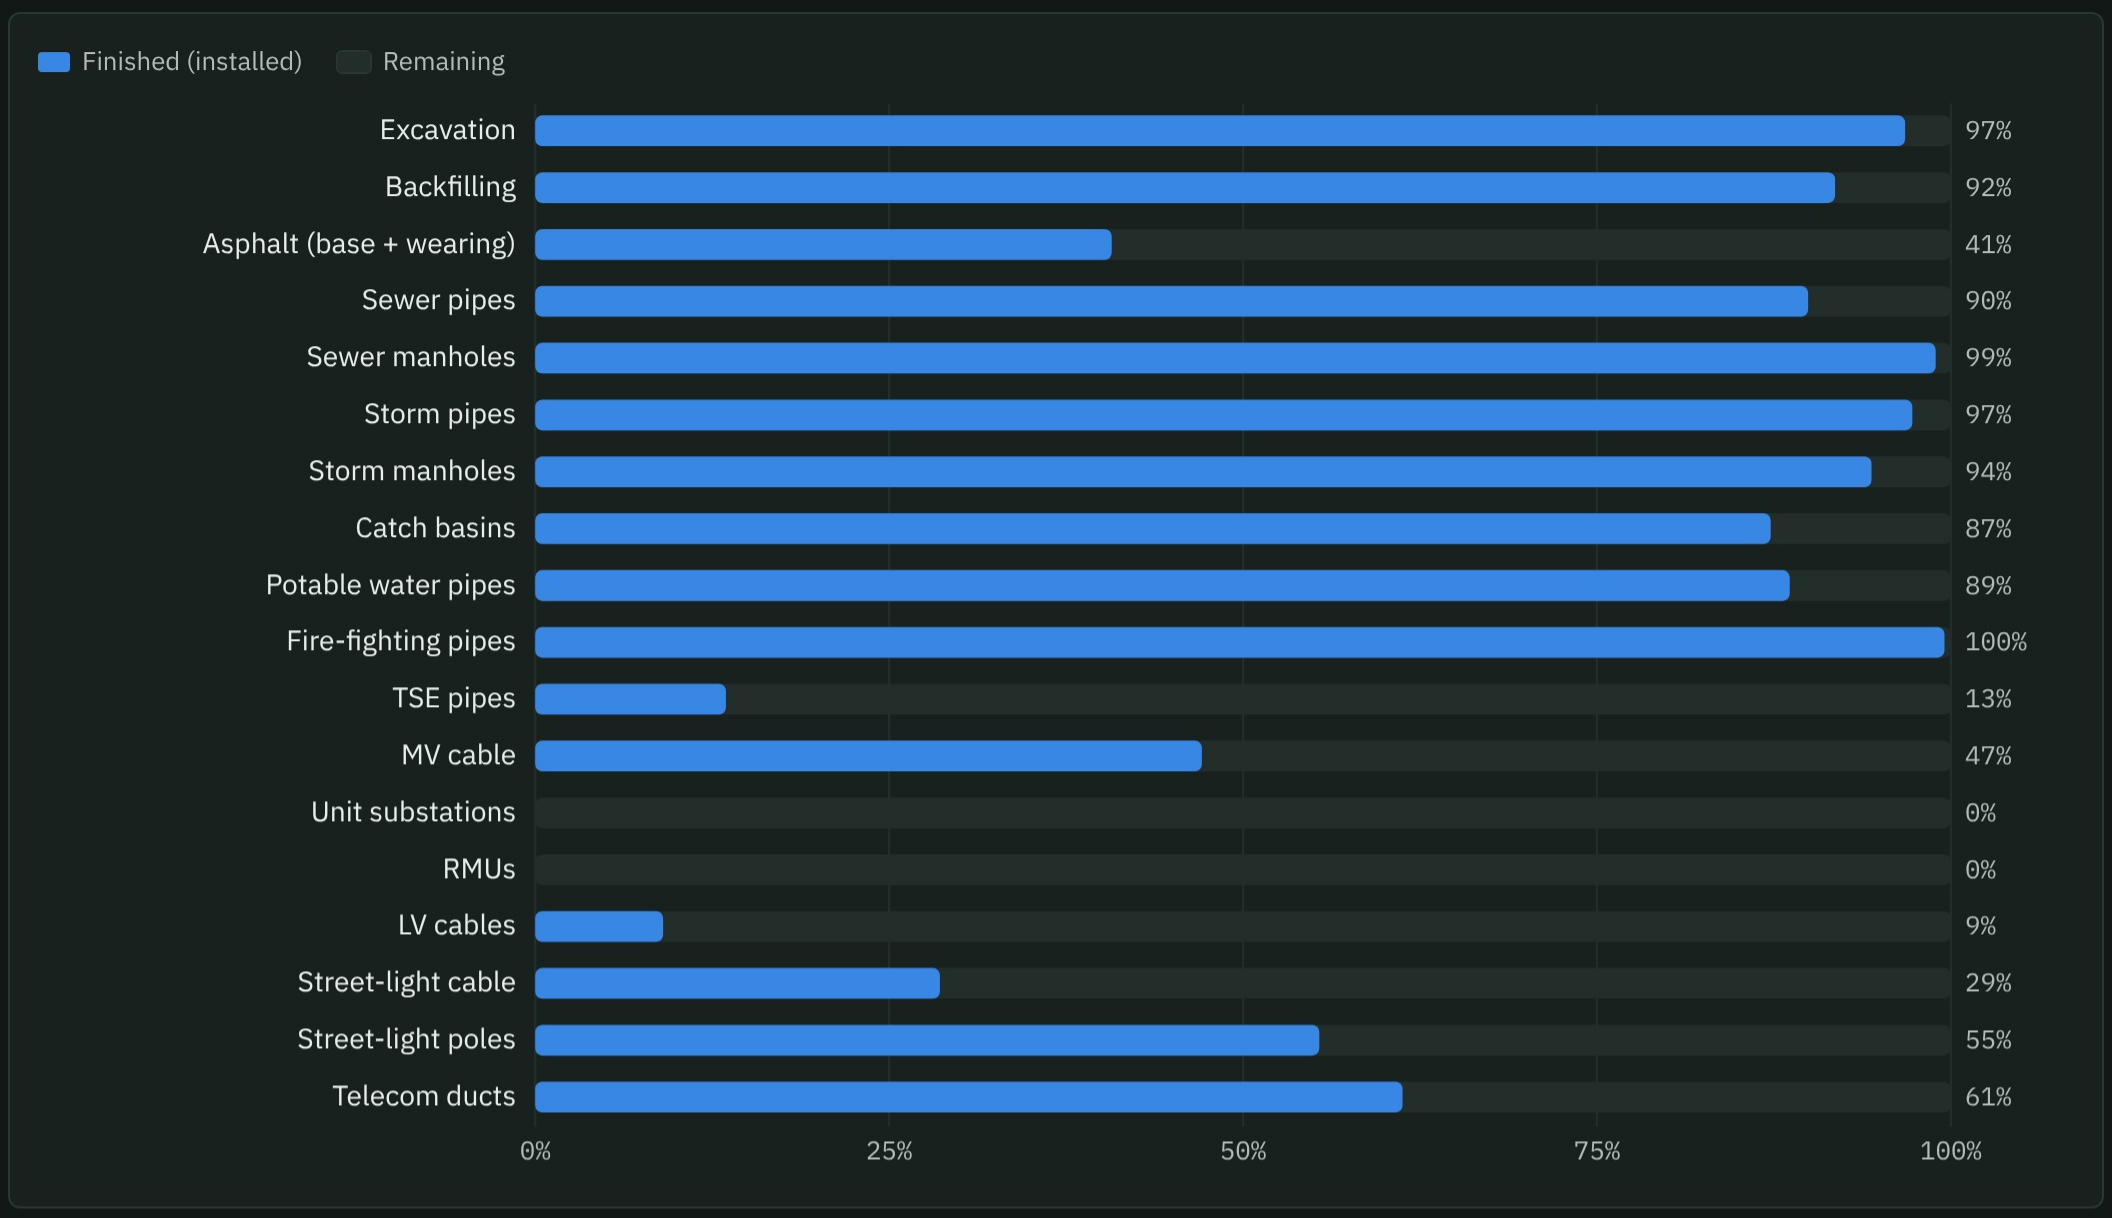

SCOPE ITEM	ZONE	UNIT	TOTAL	FINISHED	THIS WEEK	REMAINING	% FINISHED	BACKFILLED
Excavation	All	m³	853,395	825,821	0	27,574	96.8%	–
Backfilling	All	m³	1,481,028	1,359,876	+1,652	121,152	91.8%	–
Asphalt (base + wearing)	All	m³	64,334	26,201	+109.5	38,133	40.7%	–
Sewer pipes	All	LM	7,567	6,804	+0.9	763	89.9%	–
Sewer manholes	All	EA	136	134.5	+0.2	1.5	98.9%	–
Storm pipes	All	LM	14,821	14,418	+309.4	403.6	97.3%	–
Storm manholes	All	EA	160	151	+2.9	9	94.4%	–
Catch basins	All	EA	338	295	+3.7	43	87.3%	–
Potable water pipes	All	LM	7,214	6,393	+480.2	821.2	88.6%	–
Fire-fighting pipes	All	LM	6,355	6,326	+197	28.7	99.5%	–
TSE pipes	All	LM	57,419	7,737	0	49,682	13.5%	–
MV cable	All	LM	12,559	5,914	+398.9	6,645	47.1%	–
Unit substations	All	EA	3	0	0	3	0.0%	–
RMUs	All	EA	3	0	0	3	0.0%	–
LV cables	All	LM	14,370	1,299	+175.3	13,071	9.0%	–
Street-light cable	All	LM	21,525	6,154	+1,156	15,371	28.6%	–
Street-light poles	All	EA	565	312.9	+19.9	252.1	55.4%	–
Telecom ducts	All	LM	11,057	6,774	+54.2	4,283	61.3%	–

Wet networks and street lighting moved most

Potable water pipes rose by 480 LM to 88.6%, storm pipes by 309 LM to 97.3% and fire-fighting pipes by 197 LM to 99.6%. Street-light cable rose by 1,156 LM to 28.6% and MV cable by 399 LM to 47.1%.

Asphalt, TSE and LV are far behind

Asphalt is 26,201 m³ against 57,161 m³ planned to date (40.7% of the total), with only 109 m³ added this week. TSE pipes have not moved for two weeks (13.5%), LV cables are at 9.0% and telecom ducts gained only 54 LM. None of the 3 unit substations or 3 RMUs is installed.

Milestones

Baseline and forecast from the weekly report's Milestones sheet; P6 dates and total float from the P6 update with data date 03-Nov-2026.


MILESTONE	BASELINE	WEEKLY REPORT FORECAST	P6 UPDATE FORECAST	P6 FLOAT (DAYS)	STATUS
Site handover	30-Jul-2025	30-Jul-2025	30-Jul-2025 (actual)	–	✓ Done
Complete mobilisation	30-Aug-2025	30-Aug-2025	25-Nov-2025 (actual)	–	✓ Done
Complete earthworks	15-Sep-2026	08-Sep-2026 (−7 d)	–	–	? Forecast date passed
Submittals and long-lead orders complete	24-Sep-2026	07-Nov-2026 (+44 d)	–	–	▼ Late
All equipment and materials delivered	03-Dec-2026	07-Nov-2026 (−26 d)	–	–	? Conflicts with procurement
All wet networks	22-Nov-2026	31-Dec-2026 (+39 d)	31-Dec-2026	63	▼ Late
Electrical works	24-Nov-2026	21-Dec-2026 (+27 d)	13-Jan-2027	53	▼ Late
Potable water pump station	–	–	16-Dec-2026	26	● Scheduled
Sewage lift station	–	–	27-Dec-2026	42	● Scheduled
Road works and asphalt wearing course	–	–	05-Jan-2027	5	▼ At risk
Construction finish	–	–	21-Jan-2027	10	▼ At risk
All works complete, ready for initial handover	14-Jan-2027	28-Feb-2027 (+45 d)	–	–	▼ Late
Complete demobilisation	25-Jan-2027	10-Mar-2027 (+44 d)	–	–	▼ Late
Project handover	29-Jan-2027	15-Mar-2027 (+45 d)	15-Mar-2027	0	▼ Late

The P6 update finishes the project on 15-Mar-2027, 45 days after the contract completion date.

Most P6 milestones moved another 7 days later with the data date; storm water now finishes earlier (28-Nov-2026, previously 06-Dec-2026) and potable water stays at 05-Dec-2026. The schedule has no finish constraint at the contract date, so its float is measured against its own late finish. The asphalt wearing course has 5 days of float and construction finish 10 days. Other forecasts in this week's files: 28-Feb-2027 (General Information sheet), 20-Dec-2026 (recovery schedule in the progress presentation) and 30-Nov-2026 (look-ahead sheet).

Procurement of key materials

Share of each long-lead item delivered to site. Source: weekly procurement update 03-Nov-2026. By discipline (Quality-Stat sheet), 114 of 160 materials are on site: civil and roads 61 of 82, electrical 22 of 30, mechanical 31 of 48.

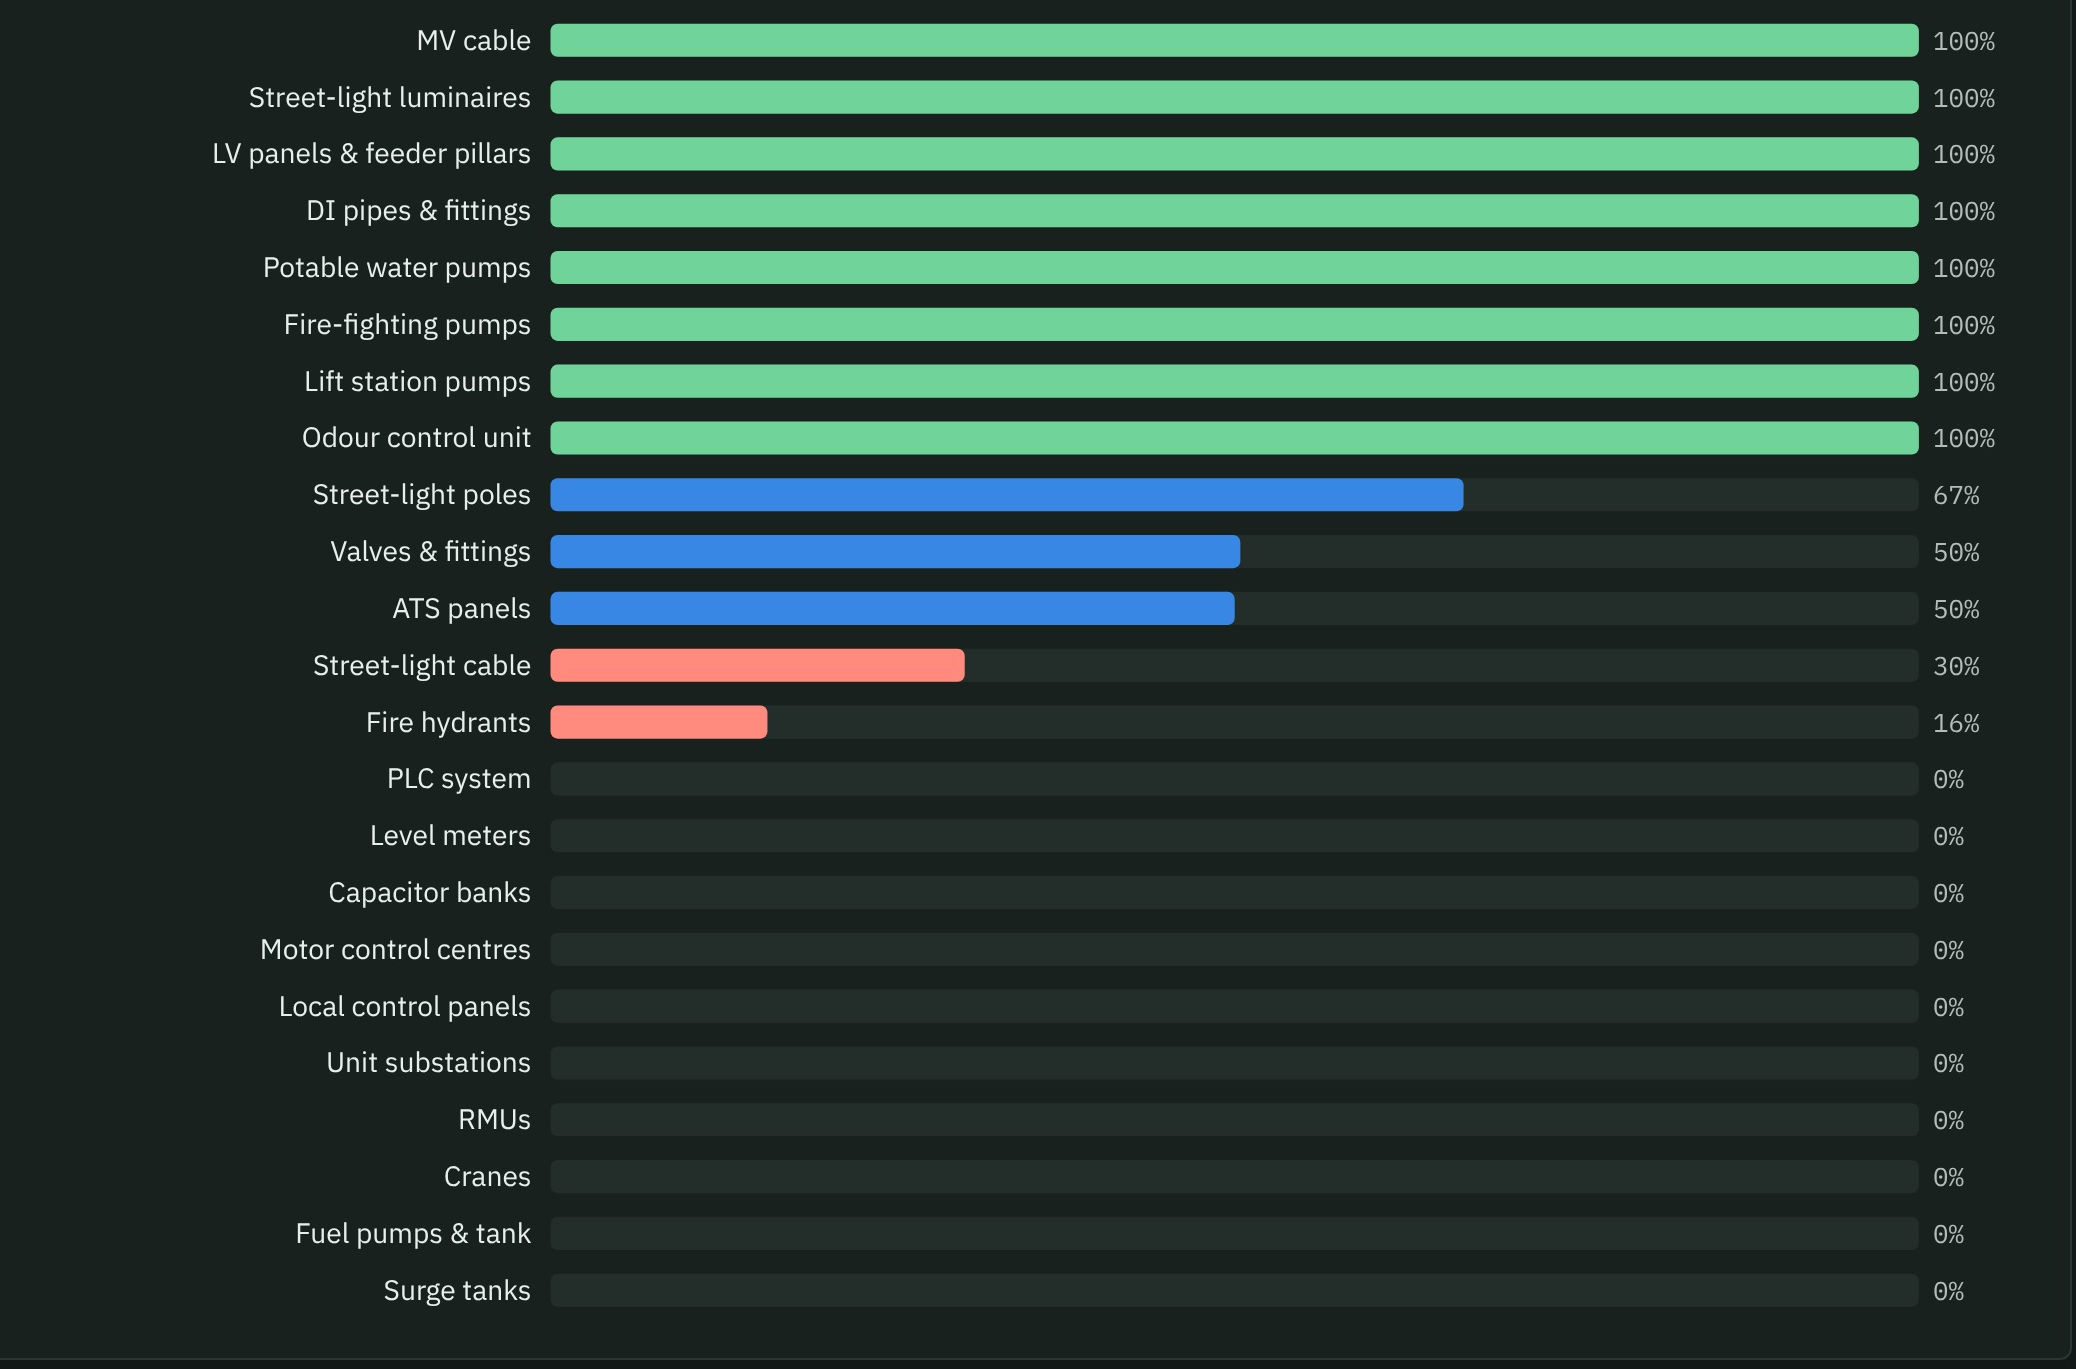

No long-lead deliveries this week


Every delivered quantity is the same as on 27-Oct. The 3 unit substations still show 30-Oct-2026, which has passed; the 5 RMUs moved to 15-Nov-2026. The capacitor banks, MCCs, local control panels, PLC system, level meters, valves and surge tanks all moved to 30-Nov-2026.

Delivery completion dates moved by two months

Planned delivery completion is now 27-Nov-2026 for electrical, 28-Nov-2026 for mechanical and 09-Dec-2026 for civil and roads materials (previously 27 and 28 Sep and 09 Nov 2026). Only 13 of 82 fire hydrants are delivered against a date of 07-Jul-2026. Materials approval: 145 of 160 approved, 3 pending.

Manpower

Monthly head count on site (staff plus labour), planned vs actual. Source: Manpower sheet.

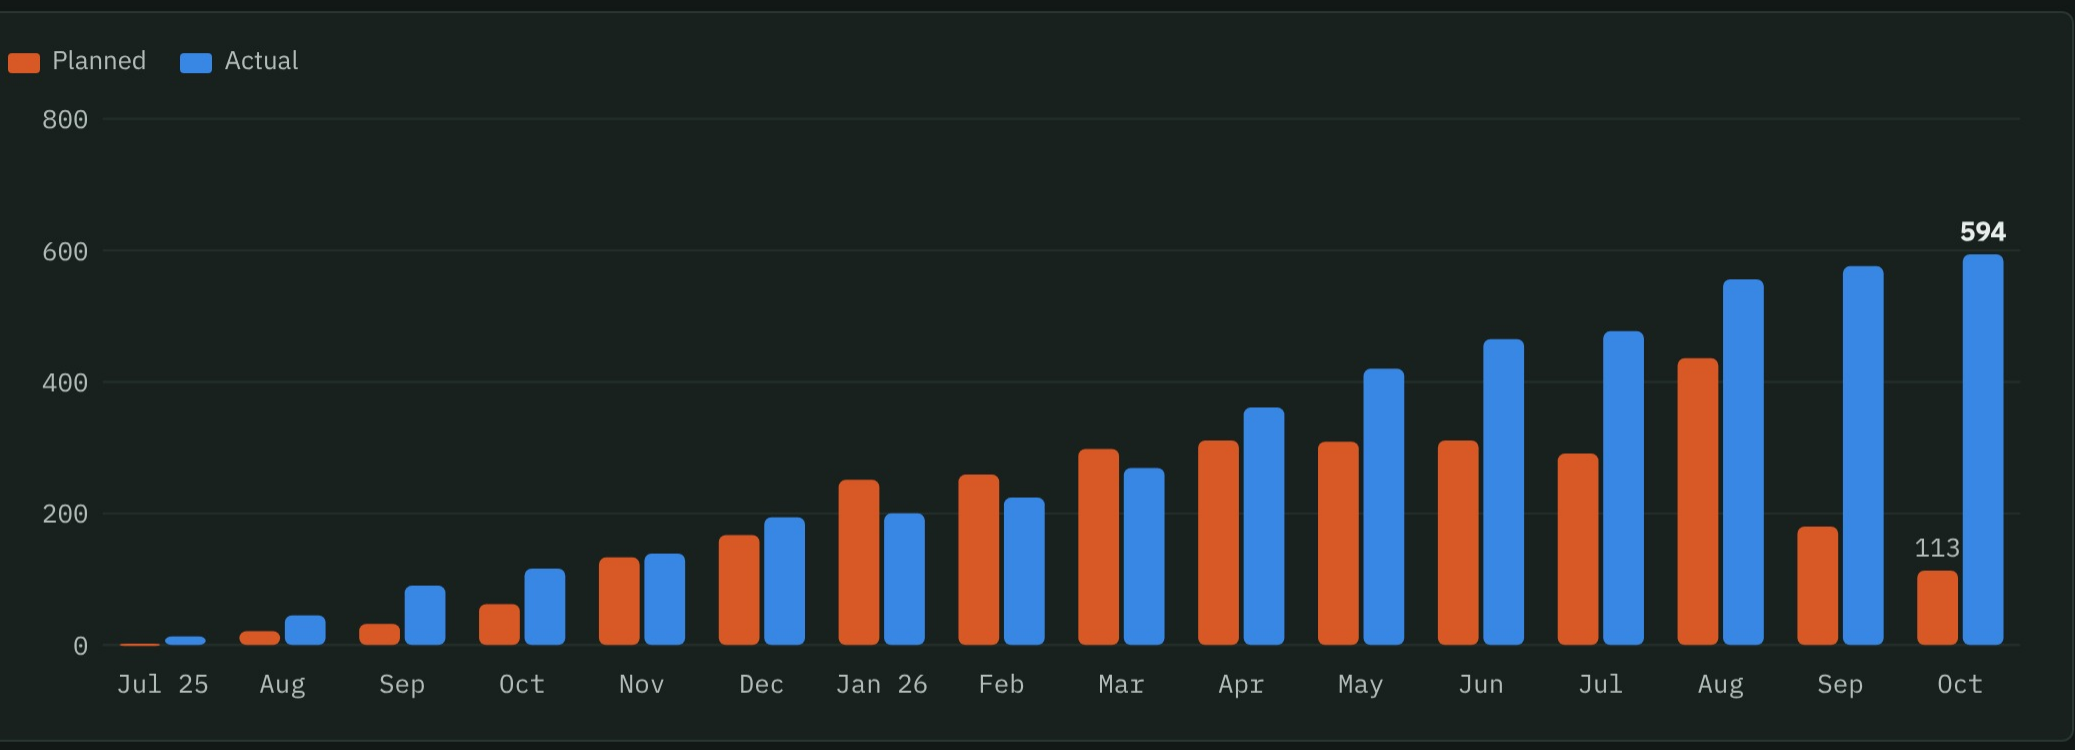

October head count was 594 (57 staff and 537 labour) against 113 planned. The November actual is not yet entered in the Manpower sheet (shown as 0); the November plan is 113 and the contractor's forecast 584. The progress presentation lists 537 workers and 330 items of equipment on site.

Cost and invoicing

Contract value

Original contract value	198,906,162.61
Revised contract value	198,906,162.61
Change orders	0

All values in SAR. The change order log is empty and potential changes are 0.

Invoices

Invoices submitted	7
Gross value	62,889,673.53
Deductions and penalties	−104,500
Net incl. VAT	72,218,624.56
Approved by consultant (CM)	7
Approved by MODON PM / paid	0 / 0

Invoicing is 31.6% of the contract value against 62.1% physical progress. No new invoice has been submitted since the period ending 15-Sep-2026. All seven invoices are approved by the consultant, but none is recorded as approved by the MODON PM or paid. The payment status needs confirming.

Health, safety and quality

Safety Score 0.93

Safe man-hours (cumulative)	944,202
Man-hours this week	34,740
Lost-time injuries	0
Fatalities	0
First-aid cases	0
Near misses	0
Property damage	0
Inductions (cumulative)	148 (895)
Toolbox talks (cumulative)	57 (4,091)

Consultant HSE inspection of 03-Nov-2026. Bracketed figures are as given in the report.

Quality Score 0.93

FIRs issued / closed / pending	5,241 / 4,994 / 247
MIRs issued / closed / pending	123 / 121 / 2
Site instructions issued / closed	52 / 42
NCRs issued / closed	51 / 51
Shop drawings approved	1,774 of 1,774
Materials approved	145 of 160

Consultant quality inspection of 03-Nov-2026. This week 327 FIRs and 3 MIRs were added and the last open NCR was closed. The front page of the report still shows 4 NCRs issued and 3 closed.

Open issues and risks

ISSUE	OWNER	DETAIL
Shortage of labour and equipment; subcontractor stopped work	Contractor	Part of the project was assigned to another contractor and the company is providing its own labour; the progress presentation gives 537 workers, 306 items of equipment and 24 dewatering pumps on site. Labour and equipment must keep increasing to meet MODON's targets. Open since 01-Apr-2026 (216 days).
Culvert on the arterial road delayed	Contractor	The roof slabs of 32 joints are cast and the last joint is excavated. The work still waits for SEC to approve the proposal for protecting the existing cable. Open since 01-Jun-2026 (155 days).
Networks must be finished before road works	Other	The subcontractor Unasco was removed and its approval withdrawn for not meeting MODON's targets. The contractor is working on the networks directly; its target to finish them by 19-Sep-2026 has passed. Open since 01-Jun-2026 (155 days).

The risk register lists the same three items, all open and rated high likelihood and high impact after treatment.

Data notes

- Report week: the weekly report states "Current Contract Weeks: 66 of 78" (Milestones sheet). The report serial number (WPR048) and the consultant's inspection number (48) are not the week number.
- This-week values compare this report with the 27-Oct-2026 report (previous week folder).
- Four different completion forecasts: 28-Feb-2027 (General Information sheet, −30 days), 15-Mar-2027 (Milestones sheet and P6 update, −45 days), 20-Dec-2026 (recovery schedule in the progress presentation) and 30-Nov-2026 (look-ahead sheet and the presentation's "target" date).
- The P6 update has no finish constraint, so no activity shows negative float although it finishes after the contract date. 319 in-progress activities have finish dates before the data date.
- Monthly actuals in the Physical-Chart Data sheet change every week: last week they were lowered, this week raised above their earlier values (May 29.6%, July 40.8%, September 50.3%).
- Quantities and man-hours disagree: Major Quantities adds 175 LM of LV cable this week, but the LV network earned no man-hours.
- The November head count is not entered in the Manpower sheet (0). For October, the front page shows 360 planned and 483 actual labour; the Manpower sheet shows 78 and 537.
- Mobilisation: the weekly report gives 30-Aug-2025 as actual, the P6 milestone "Mobilization - Finish" gives 25-Nov-2025.
- The "Complete earthworks" forecast of 08-Sep-2026 has passed but is still marked as a forecast, with earthworks at 96.2%. The "all materials delivered" forecast of 07-Nov-2026 conflicts with 46 of 160 materials not yet on site.
- Procurement: the civil and roads material count rose from 77 to 82 without explanation. The workbook's procurement log is still unusable and its front-page total still repeats the mechanical row. The procurement presentation lists 5 RMUs against 3 elsewhere, 377 street-light poles delivered against 380 on the lighting slide, and 13 fire hydrants against 12; the substations' date of 30-Oct-2026 has passed without change.
- NCRs: the front page shows 4 issued and 3 closed; the Quality-Stat sheet shows 51 issued and 51 closed.
- Sewer pipes are 89.9% finished in Major Quantities, 110.7% in the Conclusion sheet (6,804 of 6,146 LM) and 100% in the presentation (6,257 of 6,257 LM). Fire-fighting pipes are 100.9% in the Conclusion sheet.
- Cumulative toolbox-talk attendance fell from 9,091 to 4,091 between the two reports.
- Contract value is 198,906,162.61 on the front page and 198,906,162.312 "incl. VAT" in the Conclusion sheet. The invoice log has stray values (21,100,000, 20,900,000, 200,000) and EAC shows #REF!.
- Key submittal dates are in Feb–Mar 2024, before the contract award of 30-Jun-2025. The look-ahead sheet contains P6 data from the Hail Industrial City Phase II project, and the risk register uses project ID DAM2-01-029 and names the 3rd and 6th Industrial Cities.

- The workbook's issue 1 text still quotes 304 workers and 184 items of equipment; the presentation gives 537 workers and 306 items of equipment.
- The workbook's front page and the presentation also report cost-based progress; this report uses physical progress only.

Compiled 04-Nov-2026 from the weekly report WPR048 with data date 03-Nov-2026, its P6 update, the progress and procurement presentations of 03-Nov-2026, and the 27-Oct-2026 report for this-week values.
