

Activity ID	Activity Name	Original Duration	BL Project Start	BL Project Finish	Budgeted Total Cost	Planned Value Cost	Earned Value Cost	Schedule % Complete	Performance % Complete
44 READY BUILT FACTORIES 900 m2 IN AL DAMMAM #3		219	12-Feb-26	16-Feb-27	6,704,341.34	2,013,975.31	2,982,616.33	30.04%	44.49%
PROJECT MILESTONES		0	12-Feb-26	12-Feb-26	0.00	0.00	0.00	0%	0%
CONTRACTUAL MILESTONES		0	12-Feb-26	12-Feb-26	0.00	0.00	0.00	0%	0%
DAM3-PMS-MMS-007	Completion of Site levelling, local roads & parkings	0		12-Feb-26	0.00	0.00	0.00	100%	0%
CONSTRUCTION (67%)		219	20-May-26	16-Feb-27	6,556,145.92	1,941,488.88	2,849,240.45	29.61%	43.46%
RBF 900 SQM FACTORIES		219	20-May-26	16-Feb-27	6,210,097.38	1,902,311.33	2,679,612.18	30.63%	43.15%
BLOCK B6		161	20-May-26	05-Nov-26	562,990.88	557,781.60	278,513.51	99.07%	49.47%
STRUCTURAL		7	30-Jun-26	07-Jul-26	907.11	907.11	0.00	100%	0%
SLAB ON GRADE		7	30-Jun-26	07-Jul-26	907.11	907.11	0.00	100%	0%
DAM3-C-B6-S-757	Concrete pad	7	30-Jun-26	07-Jul-26	907.11	907.11	0.00	100%	0%
STRUCTURAL STEEL		7	06-Jun-26	21-Jun-26	26,895.20	26,895.20	0.00	100%	0%
DAM3-C-B6-SS-104	Epoxy paint to steel members at office area	7	06-Jun-26	13-Jun-26	23,161.04	23,161.04	0.00	100%	0%
DAM3-C-B6-SS-106	Epoxy paint for external platform	5	16-Jun-26	21-Jun-26	3,734.16	3,734.16	0.00	100%	0%
ARCHITECTURAL		43	07-Jul-26	13-Oct-26	429,413.55	429,413.55	249,506.01	100%	58.1%
WALL FINISHES		7	29-Sep-26	06-Oct-26	44,167.30	44,167.30	37,542.21	100%	85%
DAM3-C-B6-A-680	Paint to Plaster (Primer, Putty & First Coat)	7	29-Sep-26	06-Oct-26	44,167.30	44,167.30	37,542.21	100%	85%
DOORS & WINDOWS		16	07-Jul-26	19-Jul-26	209,357.49	209,357.49	80,047.23	100%	38.23%
DAM3-C-B6-A-101	Window (CW1)	7	07-Jul-26	14-Jul-26	94,173.21	94,173.21	80,047.23	100%	85%
DAM3-C-B6-A-640	Roll up Shutter Door	1	15-Jul-26	15-Jul-26	68,619.20	68,619.20	0.00	100%	0%
DAM3-C-B6-A-650	Supply and install (D5) 1000*2200mm single leaf steel doc	1	16-Jul-26	16-Jul-26	16,016.16	16,016.16	0.00	100%	0%
DAM3-C-B6-A-710	Supply and install (D4) 800*2200 mm single leaf aluminum	1	18-Jul-26	18-Jul-26	22,737.85	22,737.85	0.00	100%	0%
DAM3-C-B6-A-720	Supply and install (D7) 1000*2200 mm single leaf aluminur	1	19-Jul-26	19-Jul-26	7,811.07	7,811.07	0.00	100%	0%
METAL WORKS		5	08-Oct-26	13-Oct-26	175,888.76	175,888.76	131,916.57	100%	75%
DAM3-C-B6-A-760	Aluminium composite panel	5	08-Oct-26	13-Oct-26	175,888.76	175,888.76	131,916.57	100%	75%
MECHANICAL		2	28-Sep-26	29-Sep-26	1,819.51	1,819.51	1,364.63	100%	75%
SEWER AND DRAINAGE SYSTEM		2	28-Sep-26	29-Sep-26	1,819.51	1,819.51	1,364.63	100%	75%
SECOND STAGE		2	28-Sep-26	29-Sep-26	1,819.51	1,819.51	1,364.63	100%	75%
DAM3-C-B6-M-49	Installation of Electric Water Heater	2	28-Sep-26	29-Sep-26	1,819.51	1,819.51	1,364.63	100%	75%
ELECTRICAL		161	20-May-26	05-Nov-26	103,955.51	98,746.23	27,642.87	94.99%	26.59%
FIRST STAGE		161	20-May-26	01-Nov-26	69,188.18	69,188.18	27,642.87	100%	39.95%
DAM3-C-B6-E-343	Installation of Earthing and Grounding	4	04-Jul-26	07-Jul-26	19,646.47	19,646.47	17,681.82	100%	90%
DAM3-C-B6-E-413	Installation of Sleeves & Power outlet	8	20-May-26	01-Jun-26	2,920.45	2,920.45	1,460.23	100%	50%
DAM3-C-B6-E-373	Installation of Conduits and wiring outlets - Fire Alarm Syste	4	14-Oct-26	18-Oct-26	1,768.31	1,768.31	884.15	100%	50%
DAM3-C-B6-E-393	Installation of Conduites for Lighting Fixture	4	28-Oct-26	01-Nov-26	8,462.97	8,462.97	7,616.67	100%	90%
DAM3-C-B6-E-453	Installation of LV Cables	4	21-Jul-26	25-Jul-26	36,389.98	36,389.98	0.00	100%	0%
SECOND STAGE		8	28-Oct-26	05-Nov-26	34,767.34	29,558.06	0.00	85.02%	0%
DAM3-C-B6-E-503	Installation of Access Control System	4	28-Oct-26	01-Nov-26	27,616.86	27,616.86	0.00	100%	0%
DAM3-C-B6-E-513	Monitor Modules for Fire Alarm	2	02-Nov-26	03-Nov-26	3,882.38	1,941.19	0.00	50%	0%
DAM3-C-B6-E-523	Line Isolator Modules for Fire Alarm	2	04-Nov-26	05-Nov-26	185.40	0.00	0.00	0%	0%
DAM3-C-B6-E-533	Firewarning flash light with sounder; wall mounted, Weather	2	04-Nov-26	05-Nov-26	3,082.69	0.00	0.00	0%	0%
BLOCK B5		118	14-Jun-26	23-Nov-26	877,016.62	623,747.91	519,118.79	71.12%	59.19%
STRUCTURAL		7	22-Jun-26	29-Jun-26	907.11	907.11	0.00	100%	0%
SLAB ON GRADE		7	22-Jun-26	29-Jun-26	907.11	907.11	0.00	100%	0%
DAM3-C-B5-S-127	Concrete pad	7	22-Jun-26	29-Jun-26	907.11	907.11	0.00	100%	0%
STRUCTURAL STEEL		7	14-Jun-26	27-Jun-26	26,895.20	26,895.20	0.00	100%	0%
DAM3-C-B5-SS-102	Epoxy paint to steel members at office area	7	14-Jun-26	21-Jun-26	23,161.04	23,161.04	0.00	100%	0%
DAM3-C-B5-SS-104	Epoxy paint for external platform	5	22-Jun-26	27-Jun-26	3,734.16	3,734.16	0.00	100%	0%
ARCHITECTURAL		27	28-Jun-26	31-Aug-26	508,933.53	508,933.53	249,506.01	100%	49.03%

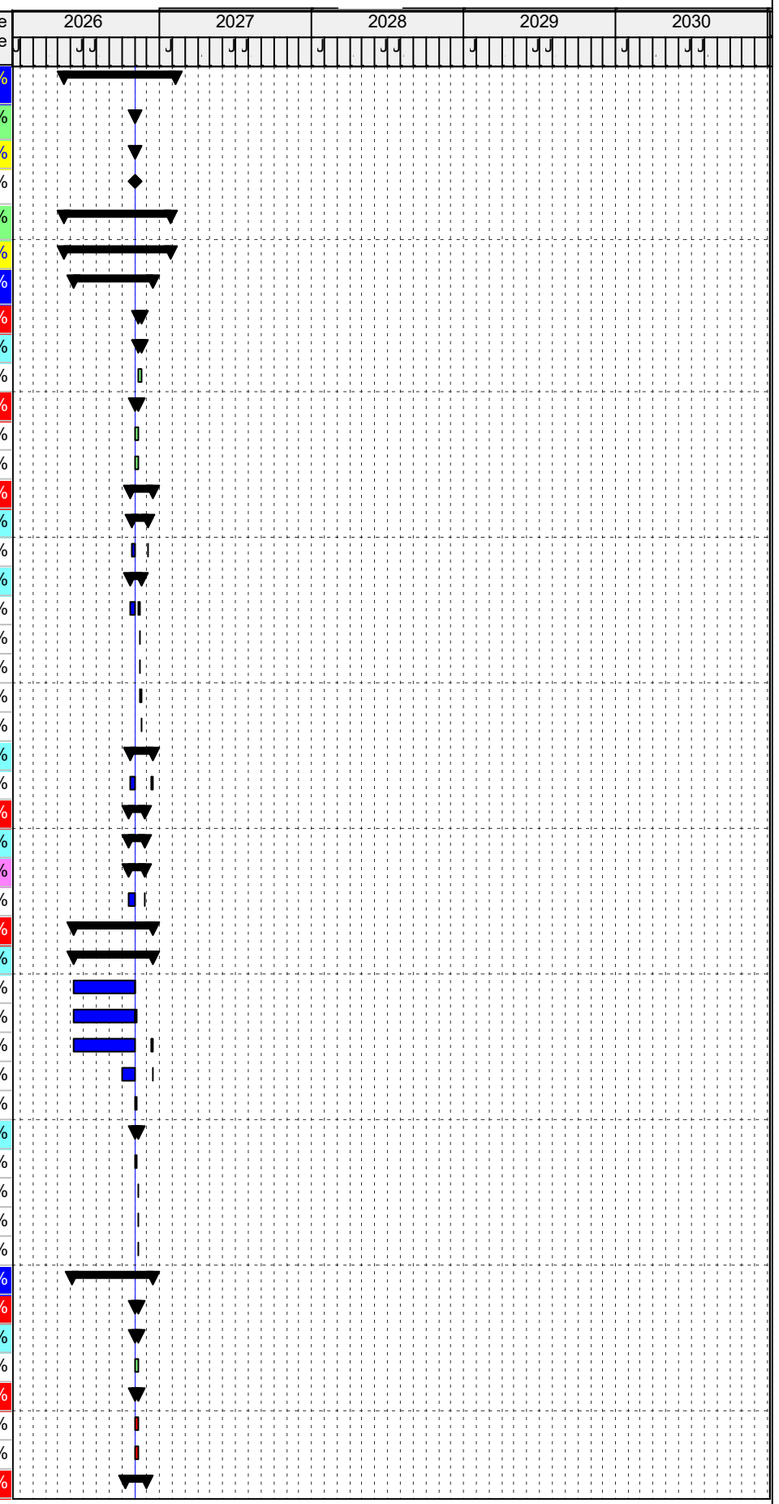

Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary

Date	Revision	Checked	Approved
03-Nov-26	2 Weeks look ahead		


Activity ID	Activity Name	Original Duration	BL Project Start	BL Project Finish	Budgeted Total Cost	Planned Value Cost	Earned Value Cost	Schedule % Complete	Performance % Complete
WALL FINISHES		7	17-Aug-26	24-Aug-26	44,167.30	44,167.30	37,542.21	100%	85%
DAM3-C-B5-A-150	Paint to Plaster (Primer, Putty & First Coat)	7	17-Aug-26	24-Aug-26	44,167.30	44,167.30	37,542.21	100%	85%
CIELING FINISHES		5	09-Aug-26	13-Aug-26	46,792.30	46,792.30	0.00	100%	0%
DAM3-C-B5-A-151	Installation of Ceiling Gypsum Board	5	09-Aug-26	13-Aug-26	46,792.30	46,792.30	0.00	100%	0%
DOORS & WINDOWS		12	28-Jun-26	12-Jul-26	242,085.17	242,085.17	80,047.23	100%	33.07%
DAM3-C-B5-A-183	Window (CW1)	7	28-Jun-26	05-Jul-26	94,173.21	94,173.21	80,047.23	100%	85%
DAM3-C-B5-A-146	Roll up Shutter Door	1	06-Jul-26	06-Jul-26	68,619.20	68,619.20	0.00	100%	0%
DAM3-C-B5-A-147	Supply and install (D5) 1000*2200mm single leaf steel doc	1	07-Jul-26	07-Jul-26	16,016.16	16,016.16	0.00	100%	0%
DAM3-C-B5-A-153	Supply and install (D4) 800*2200 mm single leaf aluminum	1	08-Jul-26	08-Jul-26	22,737.85	22,737.85	0.00	100%	0%
DAM3-C-B5-A-154	Supply and install (D7) 1000*2200 mm single leaf aluminur	1	09-Jul-26	09-Jul-26	7,811.07	7,811.07	0.00	100%	0%
DAM3-C-B5-A-176	Supply and install (D3) 1000*2200 mm single leaf aluminur	1	11-Jul-26	11-Jul-26	16,016.16	16,016.16	0.00	100%	0%
DAM3-C-B5-A-177	Supply and install fire rated 45 min (D2) 1200*2200 mm si	1	12-Jul-26	12-Jul-26	16,711.52	16,711.52	0.00	100%	0%
METAL WORKS		5	26-Aug-26	31-Aug-26	175,888.76	175,888.76	131,916.57	100%	75%
DAM3-C-B5-A-158	Aluminium composite panel	5	26-Aug-26	31-Aug-26	175,888.76	175,888.76	131,916.57	100%	75%
MECHANICAL		9	09-Aug-26	25-Aug-26	54,213.88	54,213.88	1,364.63	100%	2.52%
SEWER AND DRAINAGE SYSTEM		9	09-Aug-26	25-Aug-26	54,213.88	54,213.88	1,364.63	100%	2.52%
FIRST STAGE		2	09-Aug-26	10-Aug-26	11,055.96	11,055.96	0.00	100%	0%
DAM3-C-B5-M-11	Installation of Floor Drain	2	09-Aug-26	10-Aug-26	11,055.96	11,055.96	0.00	100%	0%
SECOND STAGE		9	17-Aug-26	25-Aug-26	43,157.92	43,157.92	1,364.63	100%	3.16%
DAM3-C-B5-M-11	Installation of Electric Water Heater	2	17-Aug-26	18-Aug-26	1,819.51	1,819.51	1,364.63	100%	75%
DAM3-C-B5-M-11	Installation of Sanitary Fixture and Accessories	4	19-Aug-26	23-Aug-26	19,921.72	19,921.72	0.00	100%	0%
DAM3-C-B5-M-11	Installation of Lavotary /Wash Basin	2	24-Aug-26	25-Aug-26	21,416.68	21,416.68	0.00	100%	0%
ELECTRICAL		118	30-Jun-26	23-Nov-26	286,066.91	32,798.20	268,248.15	11.47%	93.77%
FIRST STAGE		118	30-Jun-26	13-Oct-26	32,798.20	32,798.20	27,642.87	100%	84.28%
DAM3-C-B5-E-803	Installation of Earthing and Grounding	4	10-Oct-26	13-Oct-26	19,646.47	19,646.47	17,681.82	100%	90%
DAM3-C-B5-E-833	Installation of Conduits and wiring outlets - Fire Alarm Syste	4	01-Sep-26	05-Sep-26	1,768.31	1,768.31	884.15	100%	50%
DAM3-C-B5-E-873	Installation of Sleeves & Power outlet	8	30-Jun-26	08-Jul-26	2,920.45	2,920.45	1,460.23	100%	50%
DAM3-C-B5-E-853	Installation of Conduites for Lighting Fixture	4	15-Sep-26	19-Sep-26	8,462.97	8,462.97	7,616.67	100%	90%
SECOND STAGE		14	08-Nov-26	23-Nov-26	253,268.71	0.00	240,605.27	0%	95%
DAM3-C-B5-E-135	Installation of Solar power plant	14	08-Nov-26	23-Nov-26	253,268.71	0.00	240,605.27	0%	95%
BLOCK B4		94	28-Jun-26	01-Dec-26	534,837.67	281,568.96	223,793.15	52.65%	41.84%
STRUCTURAL STEEL		14	28-Jun-26	06-Jul-26	26,895.20	26,895.20	0.00	100%	0%
DAM3-C-B4-SS-104	Epoxy paint for external platform	5	01-Jul-26	06-Jul-26	3,734.16	3,734.16	0.00	100%	0%
DAM3-C-B4-SS-102	Epoxy paint to steel members at office area	7	28-Jun-26	05-Jul-26	23,161.04	23,161.04	0.00	100%	0%
ARCHITECTURAL		18	08-Sep-26	22-Sep-26	220,056.06	220,056.06	169,458.78	100%	77.01%
WALL FINISHES		7	08-Sep-26	15-Sep-26	44,167.30	44,167.30	37,542.21	100%	85%
DAM3-C-B4-A-109	Paint to Plaster (Primer, Putty & First Coat)	7	08-Sep-26	15-Sep-26	44,167.30	44,167.30	37,542.21	100%	85%
METAL WORKS		5	17-Sep-26	22-Sep-26	175,888.76	175,888.76	131,916.57	100%	75%
DAM3-C-B4-A-117	Aluminium composite panel	5	17-Sep-26	22-Sep-26	175,888.76	175,888.76	131,916.57	100%	75%
MECHANICAL		2	08-Sep-26	09-Sep-26	1,819.51	1,819.51	1,364.63	100%	75%
SEWER AND DRAINAGE SYSTEM		2	08-Sep-26	09-Sep-26	1,819.51	1,819.51	1,364.63	100%	75%
SECOND STAGE		2	08-Sep-26	09-Sep-26	1,819.51	1,819.51	1,364.63	100%	75%
DAM3-C-B4-M-80	Installation of Electric Water Heater	2	08-Sep-26	09-Sep-26	1,819.51	1,819.51	1,364.63	100%	75%
ELECTRICAL		94	22-Jul-26	01-Dec-26	286,066.91	32,798.20	52,969.74	11.47%	18.52%
FIRST STAGE		94	22-Jul-26	28-Oct-26	32,798.20	32,798.20	27,642.87	100%	84.28%
DAM3-C-B4-E-573	Installation of Earthing and Grounding	4	25-Oct-26	28-Oct-26	19,646.47	19,646.47	17,681.82	100%	90%
DAM3-C-B4-E-603	Installation of Conduits and wiring outlets - Fire Alarm Syste	4	24-Sep-26	28-Sep-26	1,768.31	1,768.31	884.15	100%	50%
DAM3-C-B4-E-643	Installation of Sleeves & Power outlet	8	22-Jul-26	30-Jul-26	2,920.45	2,920.45	1,460.23	100%	50%
DAM3-C-B4-E-623	Installation of Conduites for Lighting Fixture	4	08-Oct-26	12-Oct-26	8,462.97	8,462.97	7,616.67	100%	90%

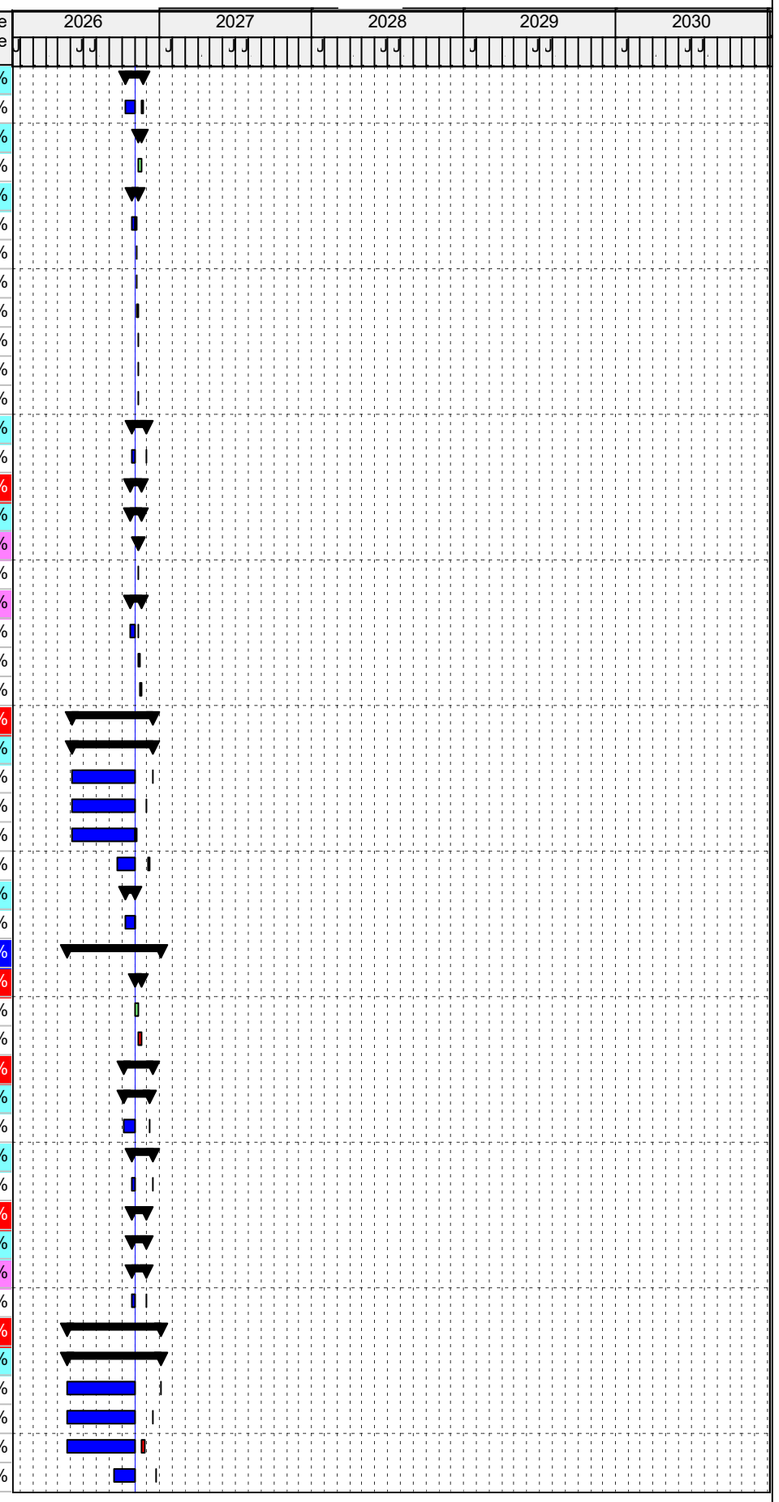

Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary

Date	Revision	Checked	Approved
03-Nov-26	2 Weeks look ahead		


Activity ID	Activity Name	Original Duration	BL Project Start	BL Project Finish	Budgeted Total Cost	Planned Value Cost	Earned Value Cost	Schedule % Complete	Performance % Complete
SECOND STAGE		7	24-Nov-26	01-Dec-26	253,268.71	0.00	25,326.87	0%	10%
DAM3-C-B4-E-104	Installation of Solar power plant	7	24-Nov-26	01-Dec-26	253,268.71	0.00	25,326.87	0%	10%
BLOCK B3		166	02-Jul-26	24-Dec-26	789,100.34	268,971.88	130,954.35	34.09%	16.6%
STRUCTURAL		7	11-Jul-26	18-Jul-26	907.11	907.11	0.00	100%	0%
SLAB ON GRADE		7	11-Jul-26	18-Jul-26	907.11	907.11	0.00	100%	0%
DAM3-C-B3-S-101	Concrete pad	7	11-Jul-26	18-Jul-26	907.11	907.11	0.00	100%	0%
STRUCTURAL STEEL		7	02-Jul-26	15-Jul-26	26,895.20	26,895.20	0.00	100%	0%
DAM3-C-B3-SS-102	Epoxy paint to steel members at office area	7	02-Jul-26	09-Jul-26	23,161.04	23,161.04	0.00	100%	0%
DAM3-C-B3-SS-104	Epoxy paint for external platform	5	11-Jul-26	15-Jul-26	3,734.16	3,734.16	0.00	100%	0%
ARCHITECTURAL		67	16-Jul-26	26-Nov-26	445,429.71	225,373.65	63,925.52	50.6%	14.35%
WALL FINISHES		2	12-Nov-26	19-Nov-26	44,167.30	0.00	37,542.21	0%	85%
DAM3-C-B3-A-109	Paint to Plaster (Primer, Putty & First Coat)	2	12-Nov-26	19-Nov-26	44,167.30	0.00	37,542.21	0%	85%
DOORS & WINDOWS		12	16-Jul-26	29-Jul-26	225,373.65	225,373.65	0.00	100%	0%
DAM3-C-B3-A-142	Window (CW1)	7	16-Jul-26	23-Jul-26	94,173.21	94,173.21	0.00	100%	0%
DAM3-C-B3-A-105	Roll up Shutter Door	1	25-Jul-26	25-Jul-26	68,619.20	68,619.20	0.00	100%	0%
DAM3-C-B3-A-106	Supply and install (D5) 1000*2200mm single leaf steel doc	1	26-Jul-26	26-Jul-26	16,016.16	16,016.16	0.00	100%	0%
DAM3-C-B3-A-112	Supply and install (D4) 800*2200 mm single leaf aluminum	1	27-Jul-26	27-Jul-26	22,737.85	22,737.85	0.00	100%	0%
DAM3-C-B3-A-113	Supply and install (D7) 1000*2200 mm single leaf aluminur	1	28-Jul-26	28-Jul-26	7,811.07	7,811.07	0.00	100%	0%
DAM3-C-B3-A-135	Supply and install (D3) 1000*2200 mm single leaf aluminur	1	29-Jul-26	29-Jul-26	16,016.16	16,016.16	0.00	100%	0%
METAL WORKS		5	22-Nov-26	26-Nov-26	175,888.76	0.00	26,383.31	0%	15%
DAM3-C-B3-A-117	Aluminium composite panel	5	22-Nov-26	26-Nov-26	175,888.76	0.00	26,383.31	0%	15%
MECHANICAL		6	27-Aug-26	06-Sep-26	12,875.47	12,875.47	1,364.63	100%	10.6%
SEWER AND DRAINAGE SYSTEM		6	27-Aug-26	06-Sep-26	12,875.47	12,875.47	1,364.63	100%	10.6%
FIRST STAGE		2	27-Aug-26	29-Aug-26	11,055.96	11,055.96	0.00	100%	0%
DAM3-C-B3-M-84	Installation of Floor Drain	2	27-Aug-26	29-Aug-26	11,055.96	11,055.96	0.00	100%	0%
SECOND STAGE		2	05-Sep-26	06-Sep-26	1,819.51	1,819.51	1,364.63	100%	75%
DAM3-C-B3-M-80	Installation of Electric Water Heater	2	05-Sep-26	06-Sep-26	1,819.51	1,819.51	1,364.63	100%	75%
ELECTRICAL		166	19-Jul-26	24-Dec-26	302,992.85	2,920.45	65,664.20	0.96%	21.67%
FIRST STAGE		166	19-Jul-26	24-Dec-26	49,724.14	2,920.45	40,337.33	5.87%	81.12%
DAM3-C-B3-E-573	Installation of Earthing and Grounding	4	21-Dec-26	24-Dec-26	19,646.47	0.00	17,681.82	0%	90%
DAM3-C-B3-E-643	Installation of Sleeves & Power outlet	5	19-Jul-26	27-Jul-26	2,920.45	2,920.45	1,460.23	100%	50%
DAM3-C-B3-E-603	Installation of Conduits and wiring outlets - Fire Alarm Syste	4	28-Nov-26	01-Dec-26	1,768.31	0.00	884.15	0%	50%
DAM3-C-B3-E-623	Installation of Conduites for Lighting Fixture	4	12-Dec-26	15-Dec-26	8,462.97	0.00	7,616.67	0%	90%
DAM3-C-B3-E-693	Installation of Wires	2	16-Dec-26	20-Dec-26	16,925.94	0.00	12,694.46	0%	75%
SECOND STAGE		7	02-Dec-26	09-Dec-26	253,268.71	0.00	25,326.87	0%	10%
DAM3-C-B3-E-104	Installation of Solar power plant	7	02-Dec-26	09-Dec-26	253,268.71	0.00	25,326.87	0%	10%
BLOCK B2		53	29-Sep-26	21-Dec-26	507,942.48	13,151.73	118,259.90	2.59%	23.28%
ARCHITECTURAL		7	16-Nov-26	01-Dec-26	220,056.06	0.00	63,925.52	0%	29.05%
WALL FINISHES		7	16-Nov-26	24-Nov-26	44,167.30	0.00	37,542.21	0%	85%
DAM3-C-B2-A-230	Paint to Plaster (Primer, Putty & First Coat)	7	16-Nov-26	24-Nov-26	44,167.30	0.00	37,542.21	0%	85%
METAL WORKS		5	25-Nov-26	01-Dec-26	175,888.76	0.00	26,383.31	0%	15%
DAM3-C-B2-A-292	Aluminium composite panel	5	25-Nov-26	01-Dec-26	175,888.76	0.00	26,383.31	0%	15%
MECHANICAL		2	16-Nov-26	18-Nov-26	1,819.51	0.00	1,364.63	0%	75%
SEWER AND DRAINAGE SYSTEM		2	16-Nov-26	18-Nov-26	1,819.51	0.00	1,364.63	0%	75%
SECOND STAGE		2	16-Nov-26	18-Nov-26	1,819.51	0.00	1,364.63	0%	75%
DAM3-C-B2-M-18	Installation of Electric Water Heater	2	16-Nov-26	18-Nov-26	1,819.51	0.00	1,364.63	0%	75%
ELECTRICAL		47	29-Sep-26	21-Dec-26	286,066.91	13,151.73	52,969.74	4.6%	18.52%
FIRST STAGE		47	29-Sep-26	11-Nov-26	32,798.20	13,151.73	27,642.87	40.1%	84.28%
DAM3-C-B2-E-143	Installation of Conduits and wiring outlets - Fire Alarm Syste	4	29-Sep-26	04-Oct-26	1,768.31	1,768.31	884.15	100%	50%

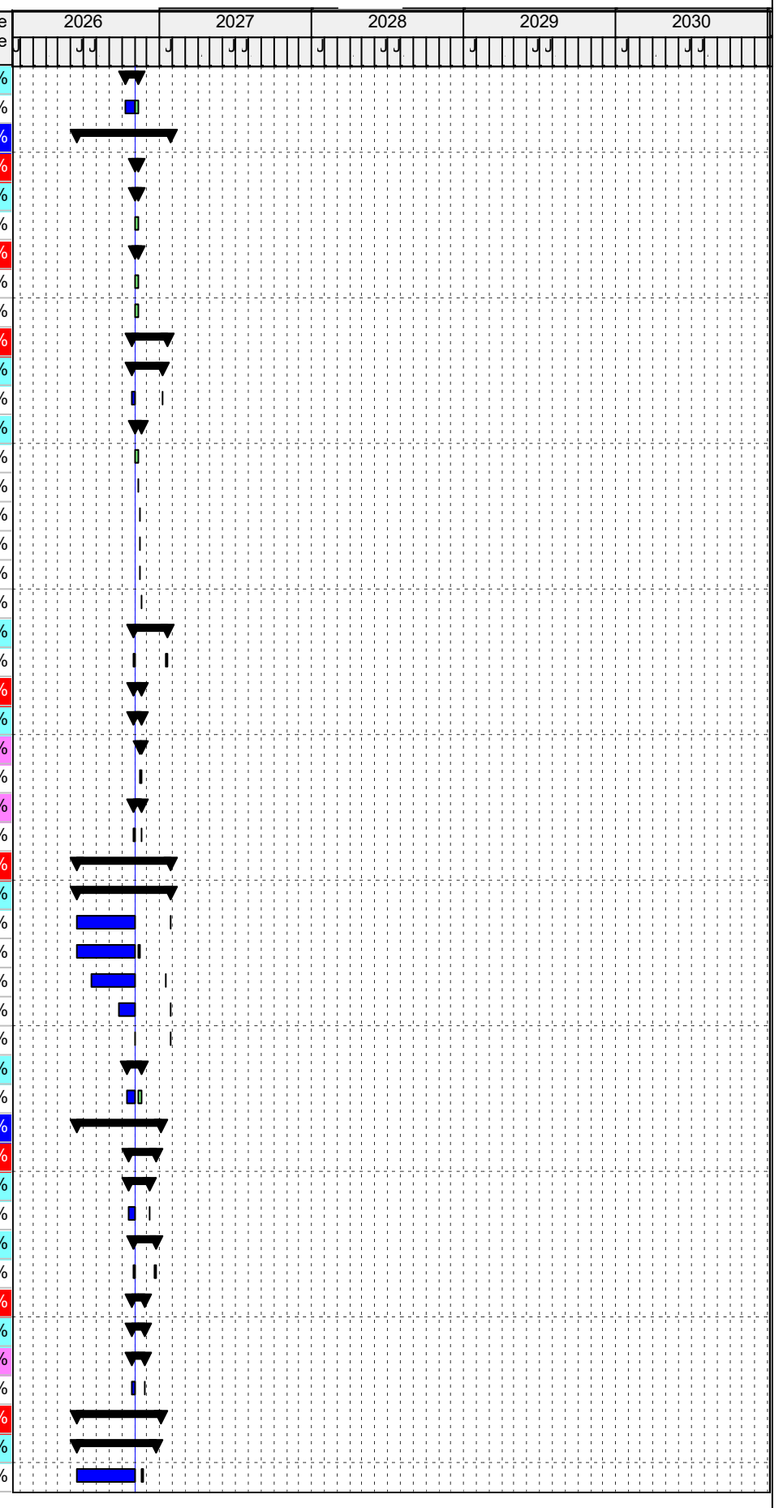

Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary

Date	Revision	Checked	Approved
03-Nov-26	2 Weeks look ahead		


Activity ID	Activity Name	Original Duration	BL Project Start	BL Project Finish	Budgeted Total Cost	Planned Value Cost	Earned Value Cost	Schedule % Complete	Performance % Complete
DAM3-C-B2-E-113	Installation of Earthing and Grounding	5	05-Nov-26	11-Nov-26	19,646.47	0.00	17,681.82	0%	90%
DAM3-C-B2-E-183	Installation of Sleeves & Power outlet	8	29-Sep-26	08-Oct-26	2,920.45	2,920.45	1,460.23	100%	50%
DAM3-C-B2-E-163	Installation of Conduites for Lighting Fixture	4	13-Oct-26	18-Oct-26	8,462.97	8,462.97	7,616.67	100%	90%
SECOND STAGE		10	10-Dec-26	21-Dec-26	253,268.71	0.00	25,326.87	0%	10%
DAM3-C-B2-E-420	Installation of Solar power plant	10	10-Dec-26	21-Dec-26	253,268.71	0.00	25,326.87	0%	10%
BLOCK B1		63	08-Oct-26	29-Dec-26	510,305.88	13,151.73	103,983.04	2.58%	20.38%
ARCHITECTURAL		26	11-Nov-26	13-Dec-26	222,419.46	0.00	49,648.67	0%	22.32%
FLOOR FINISHES		4	11-Nov-26	18-Nov-26	46,530.71	0.00	23,265.35	0%	50%
DAM3-C-B1-A-220	Tiles for Toilet	4	11-Nov-26	18-Nov-26	46,530.71	0.00	23,265.35	0%	50%
METAL WORKS		3	08-Dec-26	13-Dec-26	175,888.76	0.00	26,383.31	0%	15%
DAM3-C-B1-A-292	Aluminium composite panel	3	08-Dec-26	13-Dec-26	175,888.76	0.00	26,383.31	0%	15%
MECHANICAL		2	28-Nov-26	29-Nov-26	1,819.51	0.00	1,364.63	0%	75%
SEWER AND DRAINAGE SYSTEM		2	28-Nov-26	29-Nov-26	1,819.51	0.00	1,364.63	0%	75%
SECOND STAGE		2	28-Nov-26	29-Nov-26	1,819.51	0.00	1,364.63	0%	75%
DAM3-C-B1-M-18	Installation of Electric Water Heater	2	28-Nov-26	29-Nov-26	1,819.51	0.00	1,364.63	0%	75%
ELECTRICAL		63	08-Oct-26	29-Dec-26	286,066.91	13,151.73	52,969.74	4.6%	18.52%
FIRST STAGE		41	08-Oct-26	22-Nov-26	32,798.20	13,151.73	27,642.87	40.1%	84.28%
DAM3-C-B1-E-113	Installation of Earthing and Grounding	5	16-Nov-26	22-Nov-26	19,646.47	0.00	17,681.82	0%	90%
DAM3-C-B1-E-183	Installation of Sleeves & Power outlet	8	08-Oct-26	17-Oct-26	2,920.45	2,920.45	1,460.23	100%	50%
DAM3-C-B1-E-143	Installation of Conduits and wiring outlets - Fire Alarm Syste	4	08-Oct-26	12-Oct-26	1,768.31	1,768.31	884.15	100%	50%
DAM3-C-B1-E-163	Installation of Conduites for Lighting Fixture	4	22-Oct-26	26-Oct-26	8,462.97	8,462.97	7,616.67	100%	90%
SECOND STAGE		7	22-Dec-26	29-Dec-26	253,268.71	0.00	25,326.87	0%	10%
DAM3-C-B1-E-420	Installation of Solar power plant	7	22-Dec-26	29-Dec-26	253,268.71	0.00	25,326.87	0%	10%
BLOCK B7		63	27-Sep-26	28-Nov-26	381,670.40	122,046.15	254,458.29	31.98%	66.67%
ARCHITECTURAL		20	04-Oct-26	28-Nov-26	252,783.74	32,727.68	194,004.54	12.95%	76.75%
WALL FINISHES		4	14-Nov-26	21-Nov-26	44,167.30	0.00	37,542.21	0%	85%
DAM3-C-B7-A-230	Paint to Plaster (Primer, Putty & First Coat)	4	14-Nov-26	21-Nov-26	44,167.30	0.00	37,542.21	0%	85%
DOORS & WINDOWS		5	04-Oct-26	08-Oct-26	32,727.68	32,727.68	24,545.76	100%	75%
DAM3-C-B7-A-200	Supply and install (D5) 1000*2200mm single leaf steel doc	1	04-Oct-26	04-Oct-26	16,016.16	16,016.16	12,012.12	100%	75%
DAM3-C-B7-A-557	Supply and install fire rated 45 min (D2) 1200*2200 mm si	1	08-Oct-26	08-Oct-26	16,711.52	16,711.52	12,533.64	100%	75%
METAL WORKS		5	23-Nov-26	28-Nov-26	175,888.76	0.00	131,916.57	0%	75%
DAM3-C-B7-A-292	Aluminium composite panel	5	23-Nov-26	28-Nov-26	175,888.76	0.00	131,916.57	0%	75%
MECHANICAL		4	16-Nov-26	19-Nov-26	19,921.72	0.00	9,960.86	0%	50%
SEWER AND DRAINAGE SYSTEM		4	16-Nov-26	19-Nov-26	19,921.72	0.00	9,960.86	0%	50%
SECOND STAGE		4	16-Nov-26	19-Nov-26	19,921.72	0.00	9,960.86	0%	50%
DAM3-C-B7-M-19	Installation of Sanitary Fixture and Accessories	4	16-Nov-26	19-Nov-26	19,921.72	0.00	9,960.86	0%	50%
ELECTRICAL		63	27-Sep-26	08-Nov-26	108,964.94	89,318.47	50,492.90	81.97%	46.34%
FIRST STAGE		63	27-Sep-26	08-Nov-26	32,798.20	13,151.73	27,642.87	40.1%	84.28%
DAM3-C-B7-E-113	Installation of Earthing and Grounding	5	03-Nov-26	08-Nov-26	19,646.47	0.00	17,681.82	0%	90%
DAM3-C-B7-E-143	Installation of Conduits and wiring outlets - Fire Alarm Syste	4	27-Sep-26	30-Sep-26	1,768.31	1,768.31	884.15	100%	50%
DAM3-C-B7-E-183	Installation of Sleeves & Power outlet	8	27-Sep-26	05-Oct-26	2,920.45	2,920.45	1,460.23	100%	50%
DAM3-C-B7-E-163	Installation of Conduites for Lighting Fixture	4	11-Oct-26	14-Oct-26	8,462.97	8,462.97	7,616.67	100%	90%
SECOND STAGE		4	20-Oct-26	24-Oct-26	76,166.74	76,166.74	22,850.02	100%	30%
DAM3-C-B7-E-153	Installation of Lighting fixtures	4	20-Oct-26	24-Oct-26	76,166.74	76,166.74	22,850.02	100%	30%
BLOCK B8		61	18-Oct-26	14-Jan-27	526,044.69	8,920.25	435,004.35	1.7%	82.69%
ARCHITECTURAL		24	05-Dec-26	19-Dec-26	220,056.06	0.00	169,458.78	0%	77.01%
WALL FINISHES		4	05-Dec-26	12-Dec-26	44,167.30	0.00	37,542.21	0%	85%
DAM3-C-B8-A-230	Paint to Plaster (Primer, Putty & First Coat)	4	05-Dec-26	12-Dec-26	44,167.30	0.00	37,542.21	0%	85%
METAL WORKS		3	14-Dec-26	19-Dec-26	175,888.76	0.00	131,916.57	0%	75%

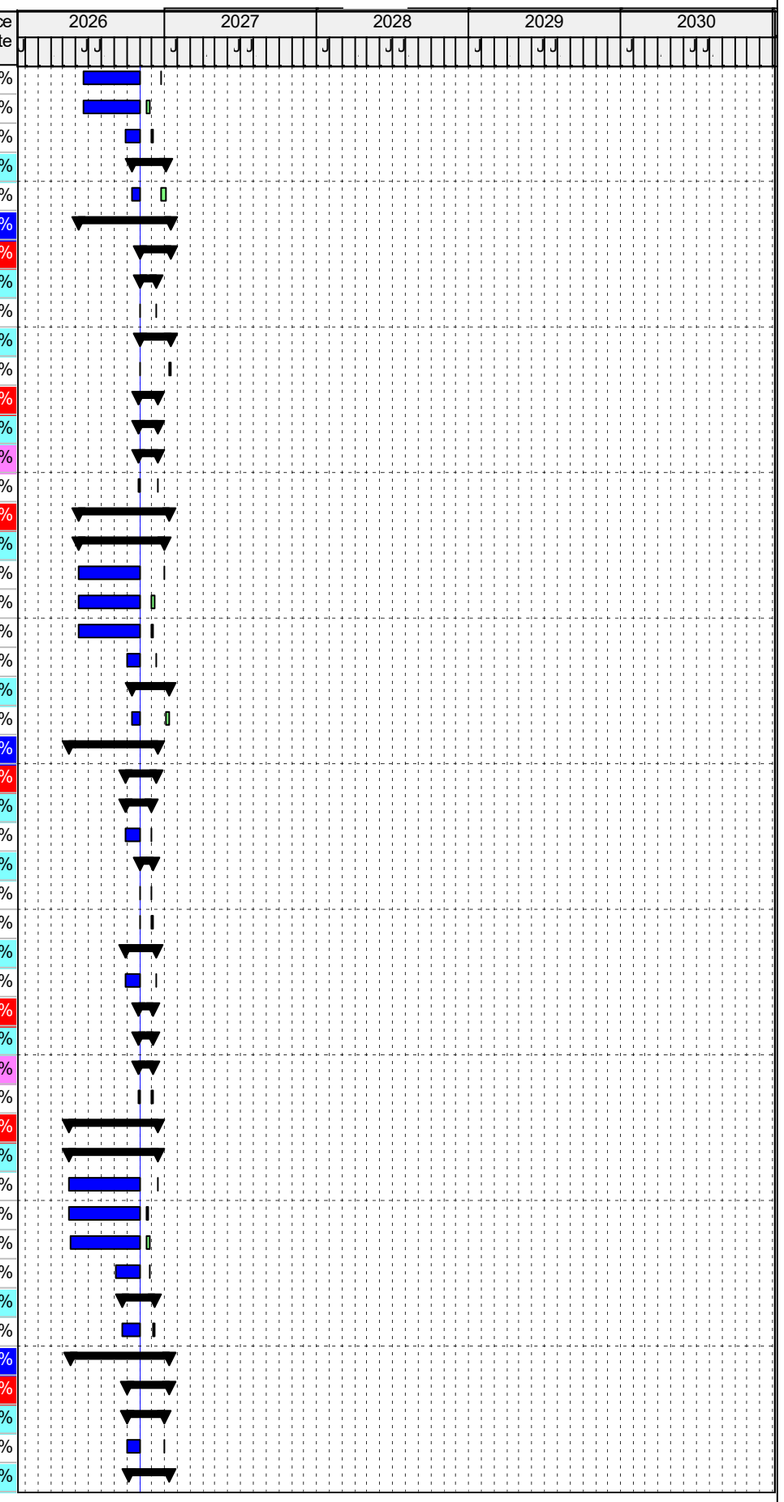

Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary

Date	Revision	Checked	Approved
03-Nov-26	2 Weeks look ahead		


Activity ID	Activity Name	Original Duration	BL Project Start	BL Project Finish	Budgeted Total Cost	Planned Value Cost	Earned Value Cost	Schedule % Complete	Performance % Complete
DAM3-C-B8-A-292	Aluminium composite panel	3	14-Dec-26	19-Dec-26	175,888.76	0.00	131,916.57	0%	75%
MECHANICAL		2	07-Dec-26	10-Dec-26	19,921.72	0.00	9,960.86	0%	50%
SEWER AND DRAINAGE SYSTEM		2	07-Dec-26	10-Dec-26	19,921.72	0.00	9,960.86	0%	50%
SECOND STAGE		2	07-Dec-26	10-Dec-26	19,921.72	0.00	9,960.86	0%	50%
DAM3-C-B8-M-19	Installation of Sanitary Fixture and Accessories	2	07-Dec-26	10-Dec-26	19,921.72	0.00	9,960.86	0%	50%
ELECTRICAL		61	18-Oct-26	14-Jan-27	286,066.91	8,920.25	255,584.71	3.12%	89.34%
FIRST STAGE		61	18-Oct-26	29-Nov-26	32,798.20	8,920.25	27,642.87	27.2%	84.28%
DAM3-C-B8-E-113	Installation of Earthing and Grounding	3	24-Nov-26	29-Nov-26	19,646.47	0.00	17,681.82	0%	90%
DAM3-C-B8-E-143	Installation of Conduits and wiring outlets - Fire Alarm Syste	4	18-Oct-26	21-Oct-26	1,768.31	1,768.31	884.15	100%	50%
DAM3-C-B8-E-183	Installation of Sleeves & Power outlet	8	18-Oct-26	26-Oct-26	2,920.45	2,920.45	1,460.23	100%	50%
DAM3-C-B8-E-163	Installation of Conduites for Lighting Fixture	4	01-Nov-26	04-Nov-26	8,462.97	4,231.49	7,616.67	50%	90%
SECOND STAGE		7	07-Jan-27	14-Jan-27	253,268.71	0.00	227,941.84	0%	90%
DAM3-C-B8-E-420	Installation of Solar power plant	7	07-Jan-27	14-Jan-27	253,268.71	0.00	227,941.84	0%	90%
BLOCK B9		77	21-Oct-26	31-Jan-27	506,122.97	4,688.76	304,391.02	0.93%	60.14%
ARCHITECTURAL		9	08-Dec-26	22-Dec-26	220,056.06	0.00	213,430.97	0%	96.99%
WALL FINISHES		4	08-Dec-26	15-Dec-26	44,167.30	0.00	37,542.21	0%	85%
DAM3-C-B9-A-230	Paint to Plaster (Primer, Putty & First Coat)	4	08-Dec-26	15-Dec-26	44,167.30	0.00	37,542.21	0%	85%
METAL WORKS		3	17-Dec-26	22-Dec-26	175,888.76	0.00	175,888.76	0%	100%
DAM3-C-B9-A-292	Aluminium composite panel	3	17-Dec-26	22-Dec-26	175,888.76	0.00	175,888.76	0%	100%
ELECTRICAL		77	21-Oct-26	31-Jan-27	286,066.91	4,688.76	90,960.05	1.64%	31.8%
FIRST STAGE		77	21-Oct-26	02-Dec-26	32,798.20	4,688.76	27,642.87	14.3%	84.28%
DAM3-C-B9-E-113	Installation of Earthing and Grounding	3	28-Nov-26	02-Dec-26	19,646.47	0.00	17,681.82	0%	90%
DAM3-C-B9-E-143	Installation of Conduits and wiring outlets - Fire Alarm Syste	4	21-Oct-26	25-Oct-26	1,768.31	1,768.31	884.15	100%	50%
DAM3-C-B9-E-183	Installation of Sleeves & Power outlet	8	21-Oct-26	29-Oct-26	2,920.45	2,920.45	1,460.23	100%	50%
DAM3-C-B9-E-163	Installation of Conduites for Lighting Fixture	4	04-Nov-26	08-Nov-26	8,462.97	0.00	7,616.67	0%	90%
SECOND STAGE		8	16-Jan-27	31-Jan-27	253,268.71	0.00	63,317.18	0%	25%
DAM3-C-B9-E-420	Installation of Solar power plant	8	16-Jan-27	31-Jan-27	253,268.71	0.00	63,317.18	0%	25%
BLOCK B10		78	25-Oct-26	08-Feb-27	506,122.97	4,688.76	154,885.57	0.93%	30.6%
ARCHITECTURAL		12	12-Dec-26	26-Dec-26	220,056.06	0.00	63,925.52	0%	29.05%
WALL FINISHES		5	12-Dec-26	19-Dec-26	44,167.30	0.00	37,542.21	0%	85%
DAM3-C-B10-A-23	Paint to Plaster (Primer, Putty & First Coat)	5	12-Dec-26	19-Dec-26	44,167.30	0.00	37,542.21	0%	85%
METAL WORKS		3	21-Dec-26	26-Dec-26	175,888.76	0.00	26,383.31	0%	15%
DAM3-C-B10-A-29	Aluminium composite panel	3	21-Dec-26	26-Dec-26	175,888.76	0.00	26,383.31	0%	15%
ELECTRICAL		78	25-Oct-26	08-Feb-27	286,066.91	4,688.76	90,960.05	1.64%	31.8%
FIRST STAGE		78	25-Oct-26	06-Dec-26	32,798.20	4,688.76	27,642.87	14.3%	84.28%
DAM3-C-B10-E-11	Installation of Earthing and Grounding	5	01-Dec-26	06-Dec-26	19,646.47	0.00	17,681.82	0%	90%
DAM3-C-B10-E-14	Installation of Conduits and wiring outlets - Fire Alarm Syste	4	25-Oct-26	28-Oct-26	1,768.31	1,768.31	884.15	100%	50%
DAM3-C-B10-E-18	Installation of Sleeves & Power outlet	4	25-Oct-26	02-Nov-26	2,920.45	2,920.45	1,460.23	100%	50%
DAM3-C-B10-E-16	Installation of Conduites for Lighting Fixture	4	08-Nov-26	11-Nov-26	8,462.97	0.00	7,616.67	0%	90%
SECOND STAGE		5	01-Feb-27	08-Feb-27	253,268.71	0.00	63,317.18	0%	25%
DAM3-C-B10-E-42	Installation of Solar power plant	5	01-Feb-27	08-Feb-27	253,268.71	0.00	63,317.18	0%	25%
BLOCK B11		125	28-Oct-26	16-Feb-27	507,942.48	3,593.59	156,250.20	0.71%	30.76%
ARCHITECTURAL		10	15-Dec-26	29-Dec-26	220,056.06	0.00	63,925.52	0%	29.05%
WALL FINISHES		4	15-Dec-26	22-Dec-26	44,167.30	0.00	37,542.21	0%	85%
DAM3-C-B11-A-23	Paint to Plaster (Primer, Putty & First Coat)	4	15-Dec-26	22-Dec-26	44,167.30	0.00	37,542.21	0%	85%
METAL WORKS		3	24-Dec-26	29-Dec-26	175,888.76	0.00	26,383.31	0%	15%
DAM3-C-B11-A-29	Aluminium composite panel	3	24-Dec-26	29-Dec-26	175,888.76	0.00	26,383.31	0%	15%
MECHANICAL		2	15-Dec-26	16-Dec-26	1,819.51	0.00	1,364.63	0%	75%
SEWER AND DRAINAGE SYSTEM		2	15-Dec-26	16-Dec-26	1,819.51	0.00	1,364.63	0%	75%

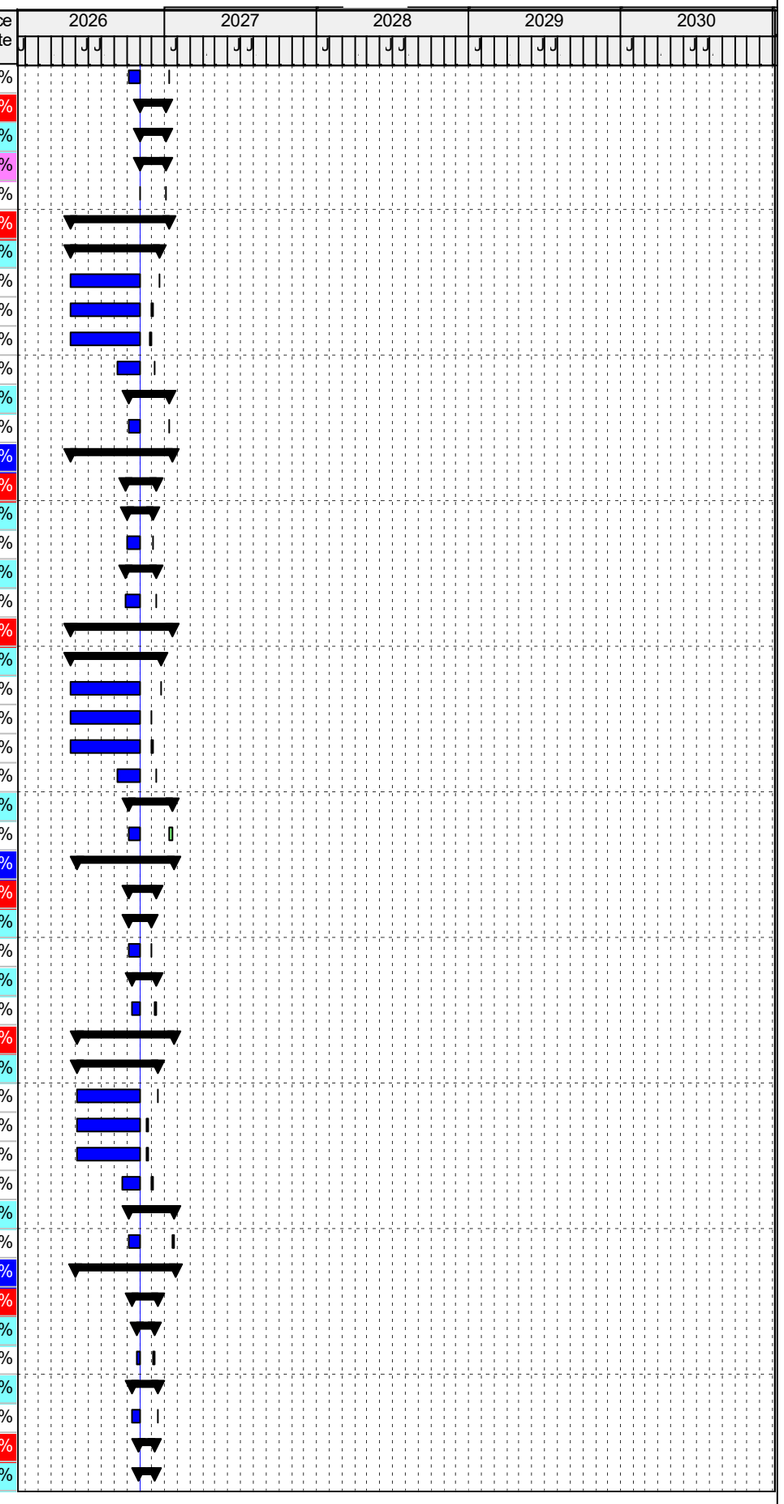

Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary

Date	Revision	Checked	Approved
03-Nov-26	2 Weeks look ahead		

Activity ID	Activity Name	Original Duration	BL Project Start	BL Project Finish	Budgeted Total Cost	Planned Value Cost	Earned Value Cost	Schedule % Complete	Performance % Complete
SECOND STAGE		2	15-Dec-26	16-Dec-26	1,819.51	0.00	1,364.63	0%	75%
DAM3-C-B11-M-1	Installation of Electric Water Heater	2	15-Dec-26	16-Dec-26	1,819.51	0.00	1,364.63	0%	75%
ELECTRICAL		125	28-Oct-26	16-Feb-27	286,066.91	3,593.59	90,960.05	1.26%	31.8%
FIRST STAGE		75	28-Oct-26	09-Dec-26	32,798.20	3,593.59	27,642.87	10.96%	84.28%
DAM3-C-B11-E-11	Installation of Earthing and Grounding	3	05-Dec-26	09-Dec-26	19,646.47	0.00	17,681.82	0%	90%
DAM3-C-B11-E-14	Installation of Conduits and wiring outlets - Fire Alarm Syste	4	28-Oct-26	01-Nov-26	1,768.31	1,768.31	884.15	100%	50%
DAM3-C-B11-E-18	Installation of Sleeves & Power outlet	8	28-Oct-26	05-Nov-26	2,920.45	1,825.28	1,460.23	62.5%	50%
DAM3-C-B11-E-16	Installation of Conduites for Lighting Fixture	4	11-Nov-26	15-Nov-26	8,462.97	0.00	7,616.67	0%	90%
SECOND STAGE		4	09-Feb-27	16-Feb-27	253,268.71	0.00	63,317.18	0%	25%
DAM3-C-B11-E-42	Installation of Solar power plant	4	09-Feb-27	16-Feb-27	253,268.71	0.00	63,317.18	0%	25%
SITE INFRASTRUCTURE		47	04-Oct-26	30-Nov-26	346,048.53	39,177.56	169,628.26	11.32%	49.02%
NETWORKS		10	19-Nov-26	30-Nov-26	53,541.58	0.00	10,708.32	0%	20%
SEWER & DRAINAGE SYSTEM		10	19-Nov-26	30-Nov-26	53,541.58	0.00	10,708.32	0%	20%
DAM3-C-ENV-SW-5	Gully trap	10	19-Nov-26	30-Nov-26	53,541.58	0.00	10,708.32	0%	20%
EXTERNAL WORKS		36	04-Oct-26	25-Nov-26	292,506.96	39,177.56	158,919.95	13.39%	54.33%
EXTERNAL ELECTRICAL WORKS		36	04-Oct-26	25-Nov-26	292,506.96	39,177.56	158,919.95	13.39%	54.33%
DAM3-C-ENV-E-42(	Installation of Sleeves for lighting poles	5	04-Oct-26	08-Oct-26	19,588.78	19,588.78	9,794.39	100%	50%
DAM3-C-ENV-E-45(	Foundation for Lighting poles	5	21-Oct-26	26-Oct-26	19,588.78	19,588.78	9,794.39	100%	50%
DAM3-C-ENV-E-46(	Electrical Manhole	7	18-Nov-26	25-Nov-26	253,329.40	0.00	139,331.17	0%	55%
TESTING AND COMMISSIONING (10%)		85	06-Oct-26	19-Jan-27	148,195.43	72,486.43	133,375.88	48.91%	90%
TESTING AND COMMISSIONING 900 Sq.m-2		7	18-Nov-26	26-Nov-26	2,987.25	0.00	2,688.52	0%	90%
MECHANICAL		7	18-Nov-26	26-Nov-26	2,987.25	0.00	2,688.52	0%	90%
P001-C-TC-M-3416	Testing and Commissioning of Electric Water Heater	7	18-Nov-26	26-Nov-26	2,987.25	0.00	2,688.52	0%	90%
TESTING AND COMMISSIONING SITE INFRASTRUCTURE		85	06-Oct-26	19-Jan-27	145,208.18	72,486.43	130,687.36	49.92%	90%
ENVIRONMENTAL		85	06-Oct-26	19-Jan-27	145,208.18	72,486.43	130,687.36	49.92%	90%
S001-C-TC-ENV-F-1(	Testing & Commissioning of External Fire Fighting System :	15	06-Oct-26	22-Oct-26	72,486.43	72,486.43	65,237.78	100%	90%
S001-C-TC-ENV-SW	Testing & Commissioning of Sewer & Drainage System	3	03-Jan-27	19-Jan-27	67,394.23	0.00	60,654.81	0%	90%
S001-C-TC-ENV-WS	Testing & Commissioning of Water Supply System	15	22-Nov-26	08-Dec-26	5,327.52	0.00	4,794.77	0%	90%

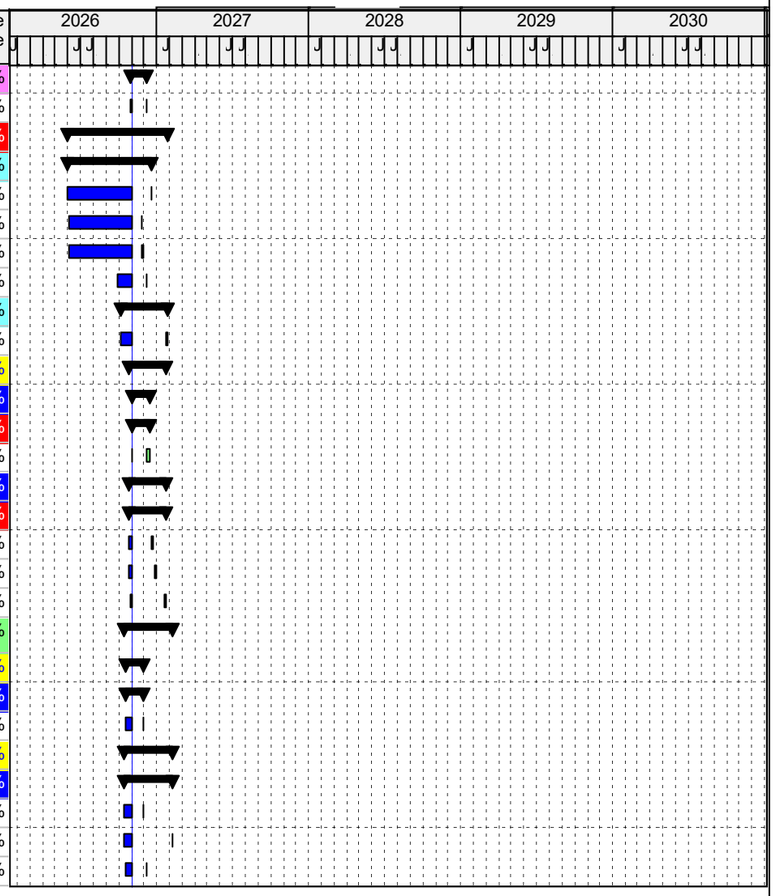

Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary

Date	Revision	Checked	Approved
03-Nov-26	2 Weeks look ahead		
