
# MLTX-02-005 - Playground Initiative for Eastern Region (Arar-Hasa osis -Dammam)

**Updateded schedule**
**D.D 28-09-2026**

| Activity ID | Activity Name | Original Duration | Schedule % Complete | Performance % Complete | BL Project Start | BL Project Finish | Start | Finish | Planned Value Cost | Earned Value Cost | Budgeted Total Cost | Variance - BL Project |
|---|---|---|---|---|---|---|---|---|---|---|---|---|
| **MLTX-02-005 - Playground Initiative for Eastern Region (Arar - Hasa Oa** | | 251 | 41.27% | 34.21% | 03-Mar-26 | 02-Jan-27 | 03-Mar-26 A | 21-Apr-27 | 12,378,902.56 | 10,262,093.38 | 29,997,851.67 | -90 |
| **KEY MILESTONES** | | 251 | 0% | 0% | 03-Mar-26 | 02-Jan-27 | 03-Mar-26 A | 21-Apr-27 | 0.00 | 0.00 | 0.00 | -90 |
| **GENERAL MILESTONES** | | 251 | 0% | 0% | 03-Mar-26 | 02-Jan-27 | 03-Mar-26 A | 21-Apr-27 | 0.00 | 0.00 | 0.00 | -90 |
| MLTX-02-005-MS-1010 | Project Commencement Date | 0 | 100% | 100% | 03-Mar-26 | | 03-Mar-26 A | | 0.00 | 0.00 | 0.00 | 0 |
| MLTX-02-005-MS-1030 | Project Completion | 0 | 0% | 0% | | 02-Jan-27 | | 21-Apr-27 | 0.00 | 0.00 | 0.00 | -90 |
| **CONTRACTUAL MILESTONE** | | 216 | 0% | 0% | 28-Mar-26 | 02-Jan-27 | 02-Apr-26 A | 08-Apr-27 | 0.00 | 0.00 | 0.00 | -79 |
| MLTX-02-005-MS-1050 | Completion of Mobilization | 0 | 100% | 100% | | 02-Apr-26 | | 02-Apr-26 A | 0.00 | 0.00 | 0.00 | 0 |
| MLTX-02-005-MS-1060 | Baseline Programme Approval | 0 | 100% | 100% | | 04-Apr-26 | | 04-Apr-26 A | 0.00 | 0.00 | 0.00 | 0 |
| MLTX-02-005-MS-1070 | Completion of Testing & Commissioning | 0 | 0% | 0% | | 26-Dec-26 | | 08-Apr-27 | 0.00 | 0.00 | 0.00 | -85 |
| MLTX-02-005-MS-1100 | Completion of Engineering | 0 | 100% | 0% | | 28-Mar-26 | | 29-Sep-26 | 0.00 | 0.00 | 0.00 | -154 |
| MLTX-02-005-MS-1120 | Completion of Levelling Works | 0 | 100% | 100% | | 04-Jun-26 | | 02-May-26 A | 0.00 | 0.00 | 0.00 | 26 |
| MLTX-02-005-MS-1130 | Completion of Toilet Building | 0 | 100% | 0% | | 26-Sep-26 | | 22-Nov-26 | 0.00 | 0.00 | 0.00 | -49 |
| MLTX-02-005-MS-1140 | Completion of Playground Area | 0 | 0% | 0% | | 02-Jan-27 | | 18-Mar-27 | 0.00 | 0.00 | 0.00 | -61 |
| MLTX-02-005-MS-1150 | Completion of Natural Landscape Works | 0 | 0% | 0% | | 19-Nov-26 | | 21-Mar-27 | 0.00 | 0.00 | 0.00 | -100 |
| MLTX-02-005-MS-1160 | Completion of Arar Works | 0 | 0% | 0% | | 04-Nov-26 | | 02-Mar-27 | 0.00 | 0.00 | 0.00 | -100 |
| MLTX-02-005-MS-1170 | Completion of Hasa Oasis Works | 0 | 0% | 0% | | 22-Dec-26 | | 25-Oct-26 | 0.00 | 0.00 | 0.00 | 50 |
| MLTX-02-005-MS-1180 | Completion of Dammam Works | 0 | 0% | 0% | | 29-Dec-26 | | 06-Apr-27 | 0.00 | 0.00 | 0.00 | -80 |
| **ARAR** | | 240 | 30.37% | 30.96% | 03-Mar-26 | 02-Jan-27 | 04-Mar-26 A | 08-Apr-27 | 3,070,829.55 | 3,129,803.79 | 10,110,715.45 | -79 |
| **MOBILIZATION** | | 23 | 0% | 0% | 03-Mar-26 | 01-Apr-26 | 04-Mar-26 A | 04-Apr-26 A | 0.00 | 0.00 | 0.00 | -2 |
| **TOPOGRAPHIC SURVEY** | | 4 | 0% | 0% | 03-Mar-26 | 07-Mar-26 | 04-Mar-26 A | 08-Mar-26 A | 0.00 | 0.00 | 0.00 | -1 |
| MLTX-02-005-MB-1320 | Site Survey Works | 4 | 100% | 100% | 03-Mar-26 | 07-Mar-26 | 04-Mar-26 A | 08-Mar-26 A | 0.00 | 0.00 | 0.00 | -1 |
| **SITE FACILITIES & OFFICES** | | 19 | 0% | 0% | 03-Mar-26 | 28-Mar-26 | 04-Mar-26 A | 02-Apr-26 A | 0.00 | 0.00 | 0.00 | -5 |
| MLTX-02-005-MB-1340 | Site Layout Plan | 3 | 100% | 100% | 03-Mar-26 | 05-Mar-26 | 04-Mar-26 A | 08-Mar-26 A | 0.00 | 0.00 | 0.00 | -2 |
| MLTX-02-005-MB-1350 | Clear & Grub for Offices & Access Road | 3 | 100% | 100% | 07-Mar-26 | 09-Mar-26 | 09-Mar-26 A | 11-Mar-26 A | 0.00 | 0.00 | 0.00 | -2 |
| MLTX-02-005-MB-1360 | Construct Site Access Roads | 3 | 100% | 100% | 07-Mar-26 | 09-Mar-26 | 09-Mar-26 A | 12-Mar-26 A | 0.00 | 0.00 | 0.00 | -3 |
| MLTX-02-005-MB-1370 | Construct Temporary Fence | 5 | 100% | 100% | 10-Mar-26 | 15-Mar-26 | 12-Mar-26 A | 19-Mar-26 A | 0.00 | 0.00 | 0.00 | -4 |
| MLTX-02-005-MB-1380 | Construct Site Offices & Storage | 10 | 100% | 100% | 10-Mar-26 | 24-Mar-26 | 14-Mar-26 A | 01-Apr-26 A | 0.00 | 0.00 | 0.00 | -7 |
| MLTX-02-005-MB-1390 | Install Project Signs | 8 | 100% | 100% | 10-Mar-26 | 18-Mar-26 | 14-Mar-26 A | 25-Mar-26 A | 0.00 | 0.00 | 0.00 | -3 |
| MLTX-02-005-MB-1400 | Install Site Facilities | 4 | 100% | 100% | 16-Mar-26 | 19-Mar-26 | 16-Mar-26 A | 28-Mar-26 A | 0.00 | 0.00 | 0.00 | -4 |
| MLTX-02-005-MB-1410 | Electrical Works & Connections | 6 | 100% | 100% | 16-Mar-26 | 25-Mar-26 | 24-Mar-26 A | 30-Mar-26 A | 0.00 | 0.00 | 0.00 | -4 |
| MLTX-02-005-MB-1420 | Construct Parking Sheds | 6 | 100% | 100% | 16-Mar-26 | 25-Mar-26 | 24-Mar-26 A | 30-Mar-26 A | 0.00 | 0.00 | 0.00 | -4 |
| MLTX-02-005-MB-1430 | Equipment Mobalization | 5 | 100% | 100% | 19-Mar-26 | 28-Mar-26 | 26-Mar-26 A | 02-Apr-26 A | 0.00 | 0.00 | 0.00 | -5 |
| MLTX-02-005-MB-1440 | Manpower Mobalization | 3 | 100% | 100% | 24-Mar-26 | 26-Mar-26 | 24-Mar-26 A | 02-Apr-26 A | 0.00 | 0.00 | 0.00 | -6 |
| **PRELIMINARY SUBMITTALS** | | 20 | 0% | 0% | 07-Mar-26 | 01-Apr-26 | 09-Mar-26 A | 04-Apr-26 A | 0.00 | 0.00 | 0.00 | -2 |
| **PREPARATIONS & SUBMITTAL BY CONTRACTORS** | | 10 | 0% | 0% | 07-Mar-26 | 17-Mar-26 | 09-Mar-26 A | 19-Mar-26 A | 0.00 | 0.00 | 0.00 | -2 |
| MLTX-02-005-MB-154 | Preparation and Submittal of Detailed Work Order | 10 | 100% | 100% | 07-Mar-26 | 17-Mar-26 | 09-Mar-26 A | 19-Mar-26 A | 0.00 | 0.00 | 0.00 | -2 |
| MLTX-02-005-MB-155 | Preparation and Submittal of Project Execution Plan | 8 | 100% | 100% | 07-Mar-26 | 15-Mar-26 | 09-Mar-26 A | 17-Mar-26 A | 0.00 | 0.00 | 0.00 | -2 |
| MLTX-02-005-MB-156 | Submission of Contractor Project Quality Plan | 8 | 100% | 100% | 07-Mar-26 | 15-Mar-26 | 09-Mar-26 A | 17-Mar-26 A | 0.00 | 0.00 | 0.00 | -2 |
| MLTX-02-005-MB-157 | Submission of Construction Safety & Environmental | 8 | 100% | 100% | 07-Mar-26 | 15-Mar-26 | 09-Mar-26 A | 17-Mar-26 A | 0.00 | 0.00 | 0.00 | -2 |
| MLTX-02-005-MB-158 | Preparation and Submittal of Organization Chart | 8 | 100% | 100% | 07-Mar-26 | 15-Mar-26 | 09-Mar-26 A | 17-Mar-26 A | 0.00 | 0.00 | 0.00 | -2 |
| MLTX-02-005-MB-159 | Preparation and Submittal of Communication Plan | 8 | 100% | 100% | 07-Mar-26 | 15-Mar-26 | 09-Mar-26 A | 17-Mar-26 A | 0.00 | 0.00 | 0.00 | -2 |
| **APPROVALS BY EMPLOYERS** | | 12 | 0% | 0% | 16-Mar-26 | 01-Apr-26 | 18-Mar-26 A | 04-Apr-26 A | 0.00 | 0.00 | 0.00 | -2 |
| MLTX-02-005-MB-168 | Approval of Detailed Work Order Programme (Baseline) | 10 | 100% | 100% | 18-Mar-26 | 01-Apr-26 | 24-Mar-26 A | 04-Apr-26 A | 0.00 | 0.00 | 0.00 | -2 |
| MLTX-02-005-MB-169 | Approval of Project Execution Plan | 10 | 100% | 100% | 16-Mar-26 | 30-Mar-26 | 18-Mar-26 A | 01-Apr-26 A | 0.00 | 0.00 | 0.00 | -2 |
| MLTX-02-005-MB-170 | Approval of Contractor Project Quality Plan | 10 | 100% | 100% | 16-Mar-26 | 30-Mar-26 | 18-Mar-26 A | 01-Apr-26 A | 0.00 | 0.00 | 0.00 | -2 |
| MLTX-02-005-MB-171 | Approval of Construction Safety & Environmental | 10 | 100% | 100% | 16-Mar-26 | 30-Mar-26 | 18-Mar-26 A | 01-Apr-26 A | 0.00 | 0.00 | 0.00 | -2 |
| MLTX-02-005-MB-172 | Approval of Organization Chart | 10 | 100% | 100% | 16-Mar-26 | 30-Mar-26 | 18-Mar-26 A | 01-Apr-26 A | 0.00 | 0.00 | 0.00 | -2 |
| MLTX-02-005-MB-173 | Approval of Communication Plan | 10 | 100% | 100% | 16-Mar-26 | 30-Mar-26 | 18-Mar-26 A | 01-Apr-26 A | 0.00 | 0.00 | 0.00 | -2 |
| **ENGINEERING** | | 196 | 0% | 0% | 07-Mar-26 | 25-Oct-26 | 07-Mar-26 A | 15-Feb-27 | 0.00 | 0.00 | 0.00 | -97 |
| **SHOP DRAWINGS** | | 195 | 0% | 0% | 08-Mar-26 | 25-Oct-26 | 07-Mar-26 A | 15-Feb-27 | 0.00 | 0.00 | 0.00 | -97 |
| **SHOP DRAWINGS SUBMISSION** | | 135 | 0% | 0% | 08-Mar-26 | 29-Jun-26 | 07-Mar-26 A | 07-Dec-26 | 0.00 | 0.00 | 0.00 | -137 |
| **SHOP DRAWING SUBMITTALS FOR EARTHING WORKS** | | 46 | 0% | 0% | 08-Mar-26 | 03-May-26 | 09-Mar-26 A | 14-Mar-26 A | 0.00 | 0.00 | 0.00 | 40 |
| MLTX-02-005-EN-1 | Shop DWG Submittal for Layout Plan | 15 | 100% | 100% | 08-Mar-26 | 28-Mar-26 | 09-Mar-26 A | 14-Mar-26 A | 0.00 | 0.00 | 0.00 | 9 |
| MLTX-02-005-EN-1 | Shop DWG Submittal for Setting Out | 16 | 100% | 100% | 08-Mar-26 | 29-Mar-26 | 09-Mar-26 A | 14-Mar-26 A | 0.00 | 0.00 | 0.00 | 10 |
| MLTX-02-005-EN-1 | Shop DWG Submittal for Grading Layout Plan | 15 | 100% | 100% | 16-Apr-26 | 03-May-26 | 09-Mar-26 A | 14-Mar-26 A | 0.00 | 0.00 | 0.00 | 40 |
| MLTX-02-005-EN-1 | Shop DWG Submittal for Curb Setting Out Points | 15 | 100% | 100% | 08-Mar-26 | 28-Mar-26 | 09-Mar-26 A | 14-Mar-26 A | 0.00 | 0.00 | 0.00 | 9 |
| MLTX-02-005-EN-1 | Shop DWG Submittal for Signing & Marking Layout Plan | 15 | 100% | 100% | 08-Mar-26 | 28-Mar-26 | 09-Mar-26 A | 14-Mar-26 A | 0.00 | 0.00 | 0.00 | 9 |
| MLTX-02-005-EN-1 | Shop DWG Submittal for Standards Details | 15 | 100% | 100% | 08-Mar-26 | 28-Mar-26 | 09-Mar-26 A | 14-Mar-26 A | 0.00 | 0.00 | 0.00 | 9 |
| **SHOP DRAWING SUBMITTALS FOR SERVICE/TOILET WORKS** | | 92 | 0% | 0% | 08-Mar-26 | 29-Jun-26 | 07-Mar-26 A | 30-Jul-26 A | 0.00 | 0.00 | 0.00 | -27 |
| **ARCHITECTURE WORKS** | | 46 | 0% | 0% | 08-Mar-26 | 03-May-26 | 09-Mar-26 A | 14-Mar-26 A | 0.00 | 0.00 | 0.00 | 40 |
| MLTX-02-005-EN | Shop DWG Submittal for Floor Plan | 15 | 100% | 100% | 08-Mar-26 | 28-Mar-26 | 09-Mar-26 A | 14-Mar-26 A | 0.00 | 0.00 | 0.00 | 9 |
| MLTX-02-005-EN | Shop DWG Submittal for Elevations | 15 | 100% | 100% | 08-Mar-26 | 28-Mar-26 | 09-Mar-26 A | 14-Mar-26 A | 0.00 | 0.00 | 0.00 | 9 |
| MLTX-02-005-EN | Shop DWG Submittal for Sections | 15 | 100% | 100% | 16-Apr-26 | 03-May-26 | 09-Mar-26 A | 14-Mar-26 A | 0.00 | 0.00 | 0.00 | 40 |




Actual Level of Effort | Actual Work | Remaining Work | Critical Remaining Work | Milestone | summary

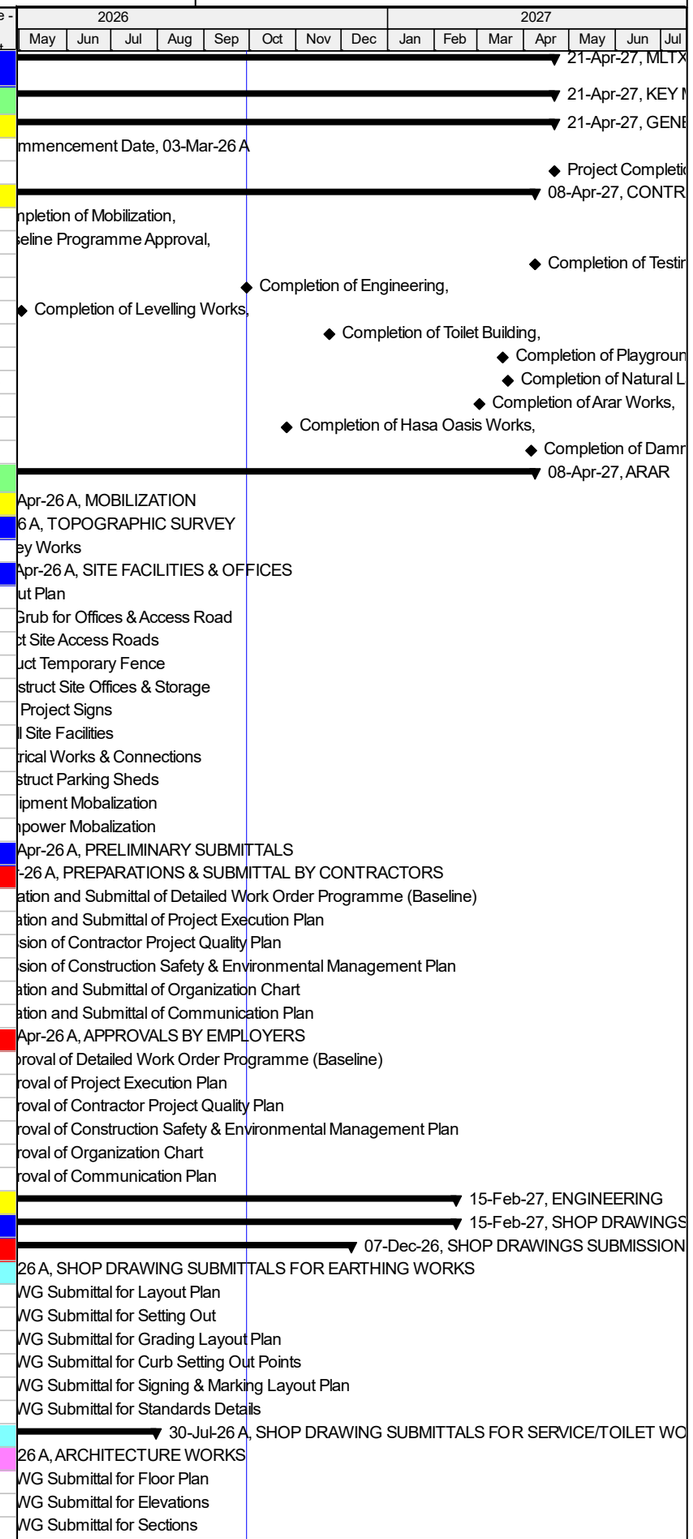


TASK filter: All Activities

© Oracle Corporation

# MLTX-02-005 - Playground Initiative for Eastern Region (Arar-Hasa osis -Dammam)

**Updateded schedule**
**D.D 28-09-2026**

| Activity ID | Activity Name | Original Duration | Schedule % Complete | Performance % Complete | BL Project Start | BL Project Finish | Start | Finish | Planned Value Cost | Earned Value Cost | Budgeted Total Cost | Variance - BL Project |
|---|---|---|---|---|---|---|---|---|---|---|---|---|
| MLTX-02-005-EM | Shop DWG Submittal for Ceiling Plan | 15 | 100% | 100% | 16-Apr-26 | 03-May-26 | 09-Mar-26 A | 14-Mar-26 A | 0.00 | 0.00 | 0.00 | 40 |
| MLTX-02-005-EM | Shop DWG Submittal for Finishes Plan | 15 | 100% | 100% | 16-Apr-26 | 03-May-26 | 09-Mar-26 A | 14-Mar-26 A | 0.00 | 0.00 | 0.00 | 40 |
| MLTX-02-005-EM | Shop DWG Submittal for Toilet Details | 15 | 100% | 100% | 16-Apr-26 | 03-May-26 | 09-Mar-26 A | 14-Mar-26 A | 0.00 | 0.00 | 0.00 | 40 |
| MLTX-02-005-EM | Shop DWG Submittal for Doors/Windows Schedule | 15 | 100% | 100% | 16-Apr-26 | 03-May-26 | 09-Mar-26 A | 14-Mar-26 A | 0.00 | 0.00 | 0.00 | 40 |
| **STRUCTURE WORKS** | | 21 | 0% | 0% | 04-May-26 | 31-May-26 | 15-Mar-26 A | 19-Mar-26 A | 0.00 | 0.00 | 0.00 | 56 |
| MLTX-02-005-EM | Shop DWG Submittal for Foundation Plan | 15 | 100% | 100% | 04-May-26 | 20-May-26 | 15-Mar-26 A | 19-Mar-26 A | 0.00 | 0.00 | 0.00 | 50 |
| MLTX-02-005-EM | Shop DWG Submittal for Ground Floor Framing Plan | 21 | 100% | 100% | 04-May-26 | 31-May-26 | 15-Mar-26 A | 19-Mar-26 A | 0.00 | 0.00 | 0.00 | 56 |
| MLTX-02-005-EM | Shop DWG Submittal for Sections/Details | 21 | 100% | 100% | 04-May-26 | 31-May-26 | 15-Mar-26 A | 19-Mar-26 A | 0.00 | 0.00 | 0.00 | 56 |
| **MECHANCAL WORKS** | | 30 | 0% | 0% | 04-May-26 | 10-Jun-26 | 07-Mar-26 A | 07-May-26 A | 0.00 | 0.00 | 0.00 | 26 |
| MLTX-02-005-EM | Shop DWG Submittal for HVAC Plan | 30 | 100% | 100% | 04-May-26 | 10-Jun-26 | 15-Mar-26 A | 19-Mar-26 A | 0.00 | 0.00 | 0.00 | 65 |
| MLTX-02-005-EM | Shop DWG Submittal for Exhaust Air Plan | 30 | 100% | 100% | 04-May-26 | 10-Jun-26 | 15-Mar-26 A | 19-Mar-26 A | 0.00 | 0.00 | 0.00 | 65 |
| MLTX-02-005-EM | Shop DWG Submittal for HVAC Equipment Schedule | 30 | 100% | 100% | 04-May-26 | 10-Jun-26 | 15-Mar-26 A | 19-Mar-26 A | 0.00 | 0.00 | 0.00 | 65 |
| MLTX-02-005-EM | Shop DWG Submittal for Drainage Layout | 30 | 100% | 100% | 04-May-26 | 10-Jun-26 | 07-Mar-26 A | 07-May-26 A | 0.00 | 0.00 | 0.00 | 26 |
| MLTX-02-005-EM | Shop DWG Submittal for Drainage Details | 30 | 100% | 100% | 04-May-26 | 10-Jun-26 | 12-Mar-26 A | 06-May-26 A | 0.00 | 0.00 | 0.00 | 27 |
| MLTX-02-005-EM | Shop DWG Submittal for Dut Routing Layout | 30 | 100% | 100% | 04-May-26 | 10-Jun-26 | 12-Mar-26 A | 04-May-26 A | 0.00 | 0.00 | 0.00 | 29 |
| MLTX-02-005-EM | Shop DWG Submittal for Diffusers Layout | 30 | 100% | 100% | 04-May-26 | 10-Jun-26 | 12-Mar-26 A | 06-May-26 A | 0.00 | 0.00 | 0.00 | 27 |
| MLTX-02-005-EM | Shop DWG Submittal for Fire Fighting Layout | 30 | 100% | 100% | 04-May-26 | 10-Jun-26 | 15-Mar-26 A | 19-Mar-26 A | 0.00 | 0.00 | 0.00 | 65 |
| MLTX-02-005-EM | Shop DWG Submittal for Water Supply Layout | 30 | 100% | 100% | 04-May-26 | 10-Jun-26 | 15-Mar-26 A | 19-Mar-26 A | 0.00 | 0.00 | 0.00 | 65 |
| MLTX-02-005-EM | Shop DWG Submittal for Water Supply Details | 30 | 100% | 100% | 04-May-26 | 10-Jun-26 | 15-Mar-26 A | 19-Mar-26 A | 0.00 | 0.00 | 0.00 | 65 |
| **ELECTRICAL WORKS** | | 64 | 0% | 0% | 04-May-26 | 29-Jun-26 | 12-Mar-26 A | 30-Jul-26 A | 0.00 | 0.00 | 0.00 | -27 |
| MLTX-02-005-EM | Shop DWG Submittal for Lighting Layout | 30 | 100% | 100% | 23-May-26 | 29-Jun-26 | 15-Mar-26 A | 19-Mar-26 A | 0.00 | 0.00 | 0.00 | 81 |
| MLTX-02-005-EM | Shop DWG Submittal for Power Layout | 30 | 100% | 100% | 04-May-26 | 10-Jun-26 | 15-Mar-26 A | 19-Mar-26 A | 0.00 | 0.00 | 0.00 | 65 |
| MLTX-02-005-EM | Shop DWG Submittal for Power Single Line Diagram | 30 | 100% | 100% | 04-May-26 | 10-Jun-26 | 12-Mar-26 A | 05-May-26 A | 0.00 | 0.00 | 0.00 | 28 |
| MLTX-02-005-EM | Shop DWG Submittal for Panel Board Schedules | 30 | 100% | 100% | 04-May-26 | 10-Jun-26 | 12-Mar-26 A | 09-May-26 A | 0.00 | 0.00 | 0.00 | 25 |
| MLTX-02-005-EM | Shop DWG Submittal for Lighting Installation Details | 30 | 100% | 100% | 04-May-26 | 10-Jun-26 | 15-Mar-26 A | 19-Mar-26 A | 0.00 | 0.00 | 0.00 | 65 |
| MLTX-02-005-EM | Shop DWG Submittal for Power Installation Details | 30 | 100% | 100% | 04-May-26 | 10-Jun-26 | 15-Mar-26 A | 19-Mar-26 A | 0.00 | 0.00 | 0.00 | 65 |
| MLTX-02-005-EM | Shop DWG Submittal for Cable Tray Installation Details | 30 | 100% | 100% | 04-May-26 | 10-Jun-26 | 12-Mar-26 A | 05-May-26 A | 0.00 | 0.00 | 0.00 | 28 |
| MLTX-02-005-EM | Shop DWG Submittal for Manhole & Ductbank Details | 30 | 100% | 100% | 04-May-26 | 10-Jun-26 | 12-Mar-26 A | 07-May-26 A | 0.00 | 0.00 | 0.00 | 26 |
| MLTX-02-005-EM | Shop DWG Submittal for Grounding Details | 30 | 100% | 100% | 04-May-26 | 10-Jun-26 | 15-Mar-26 A | 19-Mar-26 A | 0.00 | 0.00 | 0.00 | 65 |
| MLTX-02-005-EM | Shop DWG Submittal for Fire Alarm Installation Details | 30 | 100% | 100% | 04-May-26 | 10-Jun-26 | 15-Mar-26 A | 19-Mar-26 A | 0.00 | 0.00 | 0.00 | 65 |
| MLTX-02-005-EM | Shop DWG Submittal for Fire Alarm Layout | 30 | 100% | 100% | 04-May-26 | 10-Jun-26 | 15-Mar-26 A | 19-Mar-26 A | 0.00 | 0.00 | 0.00 | 65 |
| MLTX-02-005-EM | Shop DWG Submittal for Lightning Protection Details | 30 | 100% | 100% | 04-May-26 | 10-Jun-26 | 15-Mar-26 A | 19-Mar-26 A | 0.00 | 0.00 | 0.00 | 65 |
| MLTX-02-005-EM | Shop DWG Submittal for Lightning Protection System Layout | 30 | 100% | 100% | 04-May-26 | 10-Jun-26 | 15-Mar-26 A | 19-Mar-26 A | 0.00 | 0.00 | 0.00 | 65 |
| MLTX-02-005-EM | Shop DWG Submittal for Fire Alarm Riser Diagram | 30 | 100% | 100% | 04-May-26 | 10-Jun-26 | 15-Mar-26 A | 19-Mar-26 A | 0.00 | 0.00 | 0.00 | 65 |
| MLTX-02-005-EM | Shop DWG Submittal for CCTV Details | 30 | 100% | 100% | 04-May-26 | 10-Jun-26 | 30-Jul-26 A | 30-Jul-26 A | 0.00 | 0.00 | 0.00 | -43 |
| MLTX-02-005-EM | Shop DWG Submittal for CCTV Layout | 30 | 100% | 100% | 04-May-26 | 10-Jun-26 | 12-Jul-26 A | 12-Jul-26 A | 0.00 | 0.00 | 0.00 | -27 |
| MLTX-02-005-EM | Shop DWG Submittal for Telephone & Data Layout | 30 | 100% | 100% | 04-May-26 | 10-Jun-26 | 15-Mar-26 A | 19-Mar-26 A | 0.00 | 0.00 | 0.00 | 65 |
| MLTX-02-005-EM | Shop DWG Submittal for Grounding Layout | 30 | 100% | 100% | 04-May-26 | 10-Jun-26 | 15-Mar-26 A | 19-Mar-26 A | 0.00 | 0.00 | 0.00 | 65 |
| MLTX-02-005-EM | Shop DWG Submittal for CCTV Riser Diagram | 30 | 100% | 100% | 04-May-26 | 10-Jun-26 | 12-Jul-26 A | 12-Jul-26 A | 0.00 | 0.00 | 0.00 | -27 |
| MLTX-02-005-EM | Shop DWG Submittal for Telephone & Data Riser Diagram | 30 | 100% | 100% | 04-May-26 | 10-Jun-26 | 15-Mar-26 A | 19-Mar-26 A | 0.00 | 0.00 | 0.00 | 65 |
| **SHOP DRAWINGS SUBMITTALS FOR PLAYGROUND WORKS** | | 135 | 0% | 0% | 08-Mar-26 | 19-May-26 | 08-Mar-26 A | 07-Dec-26 | 0.00 | 0.00 | 0.00 | -169 |
| **ARCHITECTURE WORKS** | | 30 | 0% | 0% | 08-Mar-26 | 14-Apr-26 | 08-Mar-26 A | 25-May-26 A | 0.00 | 0.00 | 0.00 | -35 |
| MLTX-02-005-EM | Shop DWG Submittal for Playground Plan/Layout | 15 | 100% | 100% | 08-Mar-26 | 28-Mar-26 | 09-Mar-26 A | 14-Mar-26 A | 0.00 | 0.00 | 0.00 | 9 |
| MLTX-02-005-EM | Shop DWG Submittal for Furniture & Marking | 15 | 100% | 100% | 08-Mar-26 | 28-Mar-26 | 08-Mar-26 A | 12-May-26 A | 0.00 | 0.00 | 0.00 | -39 |
| MLTX-02-005-EM | Shop DWG Submittal for Sections | 15 | 100% | 100% | 08-Mar-26 | 28-Mar-26 | 09-Mar-26 A | 14-Mar-26 A | 0.00 | 0.00 | 0.00 | 9 |
| MLTX-02-005-EM | Shop DWG Submittal for Interlock Pattern Plan | 30 | 100% | 100% | 08-Mar-26 | 14-Apr-26 | 09-Mar-26 A | 14-Mar-26 A | 0.00 | 0.00 | 0.00 | 24 |
| MLTX-02-005-EM | Shop DWG Submittal for Doors/Windows Schedule | 30 | 100% | 100% | 08-Mar-26 | 14-Apr-26 | 09-Mar-26 A | 14-Mar-26 A | 0.00 | 0.00 | 0.00 | 24 |
| MLTX-02-005-EM | Shop DWG Submittal for Dome Internal Layout | 30 | 100% | 100% | 08-Mar-26 | 14-Apr-26 | 08-Mar-26 A | 25-May-26 A | 0.00 | 0.00 | 0.00 | -35 |
| **STRUCTURE WORKS** | | 45 | 0% | 0% | 15-Apr-26 | 19-May-26 | 14-Mar-26 A | 14-Jul-26 A | 0.00 | 0.00 | 0.00 | -45 |
| MLTX-02-005-EM | Shop DWG Submittal for Air Dome System | 30 | 100% | 100% | 15-Apr-26 | 19-May-26 | 14-Mar-26 A | 07-May-26 A | 0.00 | 0.00 | 0.00 | 10 |
| MLTX-02-005-EM | Shop DWG Submittal for Foundation of Air Dome | 30 | 100% | 100% | 15-Apr-26 | 19-May-26 | 14-Jul-26 A | 14-Jul-26 A | 0.00 | 0.00 | 0.00 | -44 |
| MLTX-02-005-EM | Shop DWG Submittal for Anchor Bolt Layout of Air Dome | 30 | 100% | 100% | 15-Apr-26 | 19-May-26 | 14-Jul-26 A | 14-Jul-26 A | 0.00 | 0.00 | 0.00 | -45 |
| **AIR DOME SYSTEM** | | 30 | 0% | 0% | 15-Apr-26 | 19-May-26 | 14-Mar-26 A | 24-May-26 A | 0.00 | 0.00 | 0.00 | -4 |
| MLTX-02-005-EM | Shop DWG Submittal for Air Dome Structural Layout | 30 | 100% | 100% | 15-Apr-26 | 19-May-26 | 14-Mar-26 A | 07-May-26 A | 0.00 | 0.00 | 0.00 | 10 |
| MLTX-02-005-EM | Shop DWG Submittal for Membrane Panel Layout | 30 | 100% | 100% | 15-Apr-26 | 19-May-26 | 14-Mar-26 A | 24-May-26 A | 0.00 | 0.00 | 0.00 | -4 |
| MLTX-02-005-EM | Shop DWG Submittal for Cable Tension Layout | 30 | 100% | 100% | 15-Apr-26 | 19-May-26 | 14-Mar-26 A | 24-May-26 A | 0.00 | 0.00 | 0.00 | -4 |
| MLTX-02-005-EM | Shop DWG Submittal for Airlock Door Details | 30 | 100% | 100% | 15-Apr-26 | 19-May-26 | 14-Mar-26 A | 24-May-26 A | 0.00 | 0.00 | 0.00 | -4 |
| MLTX-02-005-EM | Shop DWG Submittal for Emergency Exit Details | 30 | 100% | 100% | 15-Apr-26 | 19-May-26 | 14-Mar-26 A | 24-May-26 A | 0.00 | 0.00 | 0.00 | -4 |
| **SPORTS EQUIPMENT** | | 30 | 0% | 0% | 15-Apr-26 | 19-May-26 | 14-Mar-26 A | 25-May-26 A | 0.00 | 0.00 | 0.00 | -5 |
| MLTX-02-005-EM | Shop DWG Submittal for Football Turf Installation | 30 | 100% | 100% | 15-Apr-26 | 19-May-26 | 14-Mar-26 A | 25-May-26 A | 0.00 | 0.00 | 0.00 | -5 |
| MLTX-02-005-EM | Shop DWG Submittal for Basketball Court Marking | 30 | 100% | 100% | 15-Apr-26 | 19-May-26 | 14-Mar-26 A | 25-May-26 A | 0.00 | 0.00 | 0.00 | -5 |
| MLTX-02-005-EM | Shop DWG Submittal for Padel Court Structure | 30 | 100% | 100% | 15-Apr-26 | 19-May-26 | 14-Mar-26 A | 25-May-26 A | 0.00 | 0.00 | 0.00 | -5 |
| **MECHANCAL WORKS** | | 30 | 0% | 0% | 15-Apr-26 | 19-May-26 | 14-Mar-26 A | 03-May-26 A | 0.00 | 0.00 | 0.00 | 14 |
| MLTX-02-005-EM | Shop DWG Submittal for HVAC Plan | 30 | 100% | 100% | 15-Apr-26 | 19-May-26 | 14-Mar-26 A | 03-May-26 A | 0.00 | 0.00 | 0.00 | 14 |

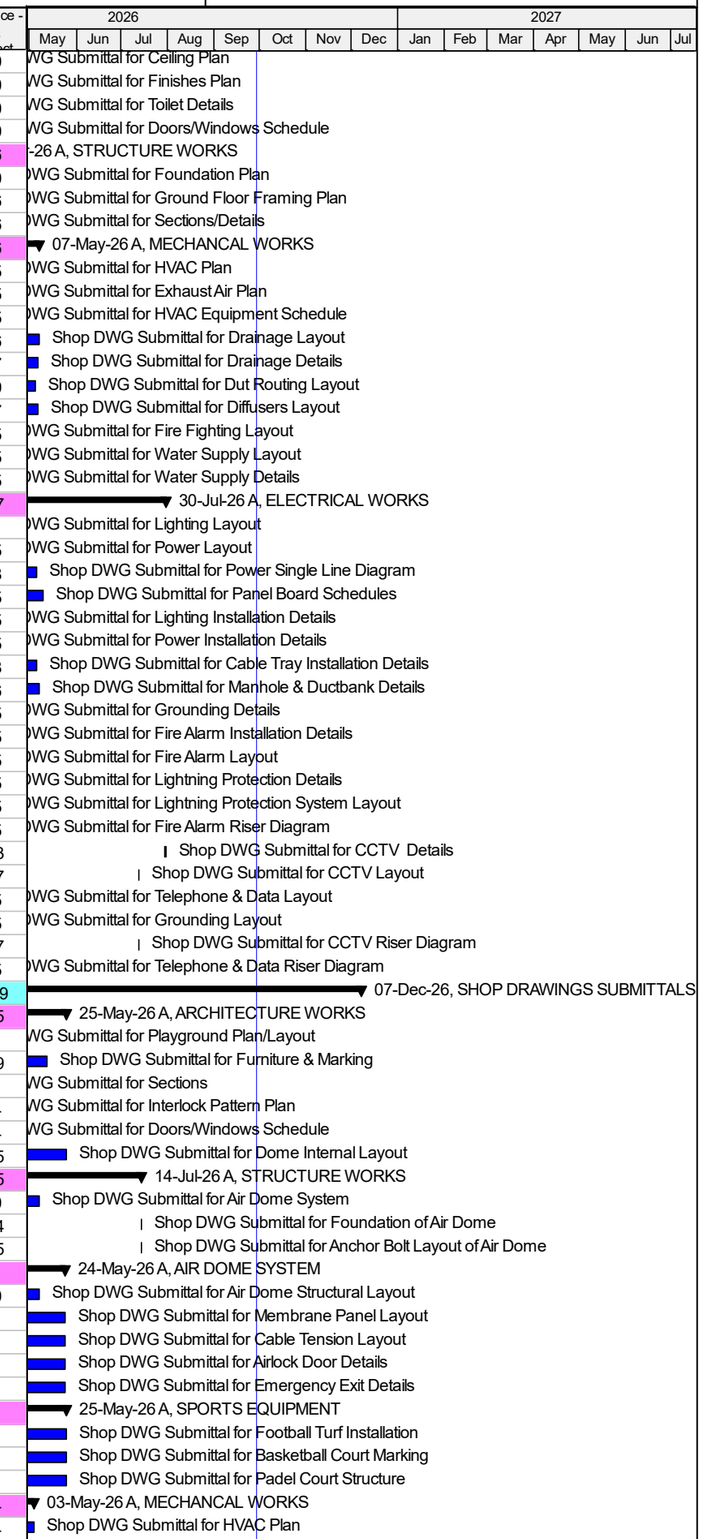


Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary




TASK filter: All Activities

© Oracle Corporation

# MLTX-02-005 - Playground Initiative for Eastern Region (Arar-Hasa osis -Dammam)

**Updateded schedule**
**D.D 28-09-2026**

| Activity ID | Activity Name | Original Duration | Schedule % Complete | Performance % Complete | BL Project Start | BL Project Finish | Start | Finish | Planned Value Cost | Earned Value Cost | Budgeted Total Cost | Variance - BL Project |
|---|---|---|---|---|---|---|---|---|---|---|---|---|
| MLTX-02-005-EN | Shop DWG Submittal for Exhaust Air Plan | 30 | 100% | 100% | 15-Apr-26 | 19-May-26 | 14-Mar-26 A | 03-May-26 A | 0.00 | 0.00 | 0.00 | 14 |
| **ELECTRICAL WORKS** | | 119 | 0% | 0% | 15-Apr-26 | 19-May-26 | 14-Mar-26 A | 07-Dec-26 | 0.00 | 0.00 | 0.00 | -169 |
| MLTX-02-005-EN | Shop DWG Submittal for Lighting Layout | 30 | 100% | 100% | 15-Apr-26 | 19-May-26 | 14-Mar-26 A | 19-Apr-26 A | 0.00 | 0.00 | 0.00 | 26 |
| MLTX-02-005-EN | Shop DWG Submittal for Power Layout | 30 | 100% | 0% | 15-Apr-26 | 19-May-26 | 29-Sep-26 | 02-Nov-26 | 0.00 | 0.00 | 0.00 | -139 |
| MLTX-02-005-EN | Shop DWG Submittal for Power Installation Details | 30 | 100% | 100% | 15-Apr-26 | 19-May-26 | 10-Jun-26 A | 10-Jun-26 A | 0.00 | 0.00 | 0.00 | -16 |
| MLTX-02-005-EN | Shop DWG Submittal for Fire Alarm Installation Details | 30 | 100% | 100% | 15-Apr-26 | 19-May-26 | 07-Jul-26 A | 07-Jul-26 A | 0.00 | 0.00 | 0.00 | -39 |
| MLTX-02-005-EN | Shop DWG Submittal for Fire Alarm Layout | 30 | 100% | 0% | 15-Apr-26 | 19-May-26 | 29-Sep-26 | 02-Nov-26 | 0.00 | 0.00 | 0.00 | -139 |
| MLTX-02-005-EN | Shop DWG Submittal for Power Single Line Diagram | 30 | 100% | 100% | 15-Apr-26 | 19-May-26 | 10-Jun-26 A | 10-Jun-26 A | 0.00 | 0.00 | 0.00 | -16 |
| MLTX-02-005-EN | Shop DWG Submittal for Panel Board Schedules | 30 | 100% | 100% | 15-Apr-26 | 19-May-26 | 10-Jun-26 A | 10-Jun-26 A | 0.00 | 0.00 | 0.00 | -16 |
| MLTX-02-005-EN | Shop DWG Submittal for Fire Alarm Riser Diagram | 30 | 100% | 0% | 15-Apr-26 | 19-May-26 | 03-Nov-26 | 07-Dec-26 | 0.00 | 0.00 | 0.00 | -169 |
| MLTX-02-005-EN | Shop DWG Submittal for CCTV Details | 30 | 100% | 100% | 15-Apr-26 | 19-May-26 | 10-Jun-26 A | 10-Jun-26 A | 0.00 | 0.00 | 0.00 | -16 |
| MLTX-02-005-EN | Shop DWG Submittal for CCTV Layout | 30 | 100% | 100% | 15-Apr-26 | 19-May-26 | 20-Aug-26 A | 20-Aug-26 A | 0.00 | 0.00 | 0.00 | -77 |
| MLTX-02-005-EN | Shop DWG Submittal for CCTV Riser Diagram | 30 | 100% | 100% | 15-Apr-26 | 19-May-26 | 20-Aug-26 A | 20-Aug-26 A | 0.00 | 0.00 | 0.00 | -77 |
| **SHOP DRAWINGS SUBMITTALS FOR LANDSCAPE WORKS** | | 46 | 0% | 0% | 08-Mar-26 | 14-Apr-26 | 08-Mar-26 A | 13-Jul-26 A | 0.00 | 0.00 | 0.00 | -74 |
| **ARCHITECTURE WORKS** | | 30 | 0% | 0% | 08-Mar-26 | 14-Apr-26 | 09-Mar-26 A | 05-May-26 A | 0.00 | 0.00 | 0.00 | -18 |
| MLTX-02-005-EN | Shop DWG Submittal for Landscape Layout | 21 | 100% | 100% | 08-Mar-26 | 04-Apr-26 | 09-Mar-26 A | 14-Mar-26 A | 0.00 | 0.00 | 0.00 | 15 |
| MLTX-02-005-EN | Shop DWG Submittal for Hardscape Plan | 21 | 100% | 100% | 08-Mar-26 | 04-Apr-26 | 09-Mar-26 A | 14-Mar-26 A | 0.00 | 0.00 | 0.00 | 15 |
| MLTX-02-005-EN | Shop DWG Submittal for Planting Plan | 15 | 100% | 100% | 29-Mar-26 | 14-Apr-26 | 14-Mar-26 A | 05-May-26 A | 0.00 | 0.00 | 0.00 | -18 |
| MLTX-02-005-EN | Shop DWG Submittal for Landscape Details | 15 | 100% | 100% | 08-Mar-26 | 28-Mar-26 | 09-Mar-26 A | 14-Mar-26 A | 0.00 | 0.00 | 0.00 | 9 |
| **MECHANCAL WORKS** | | 30 | 0% | 0% | 08-Mar-26 | 14-Apr-26 | 08-Mar-26 A | 03-Jun-26 A | 0.00 | 0.00 | 0.00 | -40 |
| MLTX-02-005-EN | Shop DWG Submittal for Irrigation Details | 30 | 100% | 100% | 08-Mar-26 | 14-Apr-26 | 08-Mar-26 A | 03-Jun-26 A | 0.00 | 0.00 | 0.00 | -40 |
| MLTX-02-005-EN | Shop DWG Submittal for Irrigation Layout | 30 | 100% | 100% | 08-Mar-26 | 14-Apr-26 | 08-Mar-26 A | 03-Jun-26 A | 0.00 | 0.00 | 0.00 | -40 |
| **ELECTRICAL WORKS** | | 30 | 0% | 0% | 08-Mar-26 | 14-Apr-26 | 12-Jul-26 A | 13-Jul-26 A | 0.00 | 0.00 | 0.00 | -74 |
| MLTX-02-005-EN | Shop DWG Submittal for Lighting Details | 30 | 100% | 100% | 08-Mar-26 | 14-Apr-26 | 13-Jul-26 A | 13-Jul-26 A | 0.00 | 0.00 | 0.00 | -74 |
| MLTX-02-005-EN | Shop DWG Submittal for Lighting Single Line Diagram | 30 | 100% | 100% | 08-Mar-26 | 14-Apr-26 | 13-Jul-26 A | 13-Jul-26 A | 0.00 | 0.00 | 0.00 | -74 |
| MLTX-02-005-EN | Shop DWG Submittal for Lighting General Arrangement | 30 | 100% | 100% | 08-Mar-26 | 14-Apr-26 | 12-Jul-26 A | 12-Jul-26 A | 0.00 | 0.00 | 0.00 | -73 |
| MLTX-02-005-EN | Shop DWG Submittal for Lighting Network Layout | 30 | 100% | 100% | 08-Mar-26 | 14-Apr-26 | 12-Jul-26 A | 12-Jul-26 A | 0.00 | 0.00 | 0.00 | -73 |
| **SHOP DRAWINGS APPROVALS** | | 185 | 0% | 0% | 29-Mar-26 | 25-Oct-26 | 14-Mar-26 A | 15-Feb-27 | 0.00 | 0.00 | 0.00 | -97 |
| **SHOP DRAWING APPROVAL FOR EARTHING WORKS** | | 47 | 0% | 0% | 29-Mar-26 | 21-May-26 | 15-Mar-26 A | 29-Mar-26 A | 0.00 | 0.00 | 0.00 | 46 |
| MLTX-02-005-EN-2 | Shop DWG Approval for Layout Plan | 15 | 100% | 100% | 29-Mar-26 | 14-Apr-26 | 15-Mar-26 A | 29-Mar-26 A | 0.00 | 0.00 | 0.00 | 14 |
| MLTX-02-005-EN-2 | Shop DWG Approval for Setting Out | 15 | 100% | 100% | 30-Mar-26 | 15-Apr-26 | 15-Mar-26 A | 29-Mar-26 A | 0.00 | 0.00 | 0.00 | 15 |
| MLTX-02-005-EN-2 | Shop DWG Approval for Grading Layout Plan | 16 | 100% | 100% | 04-May-26 | 21-May-26 | 15-Mar-26 A | 29-Mar-26 A | 0.00 | 0.00 | 0.00 | 46 |
| MLTX-02-005-EN-2 | Shop DWG Approval for Curb Setting Out Points | 15 | 100% | 100% | 29-Mar-26 | 14-Apr-26 | 15-Mar-26 A | 29-Mar-26 A | 0.00 | 0.00 | 0.00 | 14 |
| MLTX-02-005-EN-2 | Shop DWG Approval for Signing & Marking Layout Plan | 15 | 100% | 100% | 29-Mar-26 | 14-Apr-26 | 15-Mar-26 A | 29-Mar-26 A | 0.00 | 0.00 | 0.00 | 14 |
| MLTX-02-005-EN-2 | Shop DWG Approval for Standards Details | 15 | 100% | 100% | 29-Mar-26 | 14-Apr-26 | 15-Mar-26 A | 29-Mar-26 A | 0.00 | 0.00 | 0.00 | 14 |
| **SHOP DRAWING APPROVAL FOR SERVICE/TOILET WORKS** | | 107 | 0% | 0% | 29-Mar-26 | 03-Aug-26 | 15-Mar-26 A | 30-Jul-26 A | 0.00 | 0.00 | 0.00 | 3 |
| **ARCHITECTURE WORKS** | | 75 | 0% | 0% | 29-Mar-26 | 27-Jun-26 | 15-Mar-26 A | 29-Mar-26 A | 0.00 | 0.00 | 0.00 | 74 |
| MLTX-02-005-EN | Shop DWG Approval for Floor Plan | 30 | 100% | 100% | 29-Mar-26 | 02-May-26 | 15-Mar-26 A | 29-Mar-26 A | 0.00 | 0.00 | 0.00 | 29 |
| MLTX-02-005-EN | Shop DWG Approval for Elevations | 30 | 100% | 100% | 29-Mar-26 | 02-May-26 | 15-Mar-26 A | 29-Mar-26 A | 0.00 | 0.00 | 0.00 | 29 |
| MLTX-02-005-EN | Shop DWG Approval for Sections | 30 | 100% | 100% | 04-May-26 | 10-Jun-26 | 15-Mar-26 A | 29-Mar-26 A | 0.00 | 0.00 | 0.00 | 60 |
| MLTX-02-005-EN | Shop DWG Approval for Ceiling Plan | 30 | 100% | 100% | 20-May-26 | 27-Jun-26 | 15-Mar-26 A | 29-Mar-26 A | 0.00 | 0.00 | 0.00 | 74 |
| MLTX-02-005-EN | Shop DWG Approval for Finishes Plan | 30 | 100% | 100% | 04-May-26 | 10-Jun-26 | 15-Mar-26 A | 29-Mar-26 A | 0.00 | 0.00 | 0.00 | 60 |
| MLTX-02-005-EN | Shop DWG Approval for Toilet Details | 30 | 100% | 100% | 04-May-26 | 10-Jun-26 | 15-Mar-26 A | 29-Mar-26 A | 0.00 | 0.00 | 0.00 | 60 |
| MLTX-02-005-EN | Shop DWG Approval for Doors/Windows Schedule | 30 | 100% | 100% | 04-May-26 | 10-Jun-26 | 15-Mar-26 A | 29-Mar-26 A | 0.00 | 0.00 | 0.00 | 60 |
| **STRUCTURE WORKS** | | 27 | 0% | 0% | 21-May-26 | 24-Jun-26 | 24-Mar-26 A | 04-Apr-26 A | 0.00 | 0.00 | 0.00 | 67 |
| MLTX-02-005-EN | Shop DWG Approval for Foundation Plan | 4 | 100% | 100% | 21-May-26 | 25-May-26 | 24-Mar-26 A | 04-Apr-26 A | 0.00 | 0.00 | 0.00 | 44 |
| MLTX-02-005-EN | Shop DWG Approval for Ground Floor Framing Plan | 21 | 100% | 100% | 01-Jun-26 | 24-Jun-26 | 24-Mar-26 A | 04-Apr-26 A | 0.00 | 0.00 | 0.00 | 67 |
| MLTX-02-005-EN | Shop DWG Approval for Sections/Details | 21 | 100% | 100% | 01-Jun-26 | 24-Jun-26 | 24-Mar-26 A | 04-Apr-26 A | 0.00 | 0.00 | 0.00 | 67 |
| **MECHANCAL WORKS** | | 30 | 0% | 0% | 11-Jun-26 | 15-Jul-26 | 18-Mar-26 A | 10-May-26 A | 0.00 | 0.00 | 0.00 | 54 |
| MLTX-02-005-EN | Shop DWG Approval for HVAC Plan | 30 | 100% | 100% | 11-Jun-26 | 15-Jul-26 | 24-Mar-26 A | 04-Apr-26 A | 0.00 | 0.00 | 0.00 | 85 |
| MLTX-02-005-EN | Shop DWG Approval for Exhaust Air Plan | 30 | 100% | 100% | 11-Jun-26 | 15-Jul-26 | 24-Mar-26 A | 04-Apr-26 A | 0.00 | 0.00 | 0.00 | 85 |
| MLTX-02-005-EN | Shop DWG Approval for HVAC Equipment Schedule | 30 | 100% | 100% | 11-Jun-26 | 15-Jul-26 | 24-Mar-26 A | 04-Apr-26 A | 0.00 | 0.00 | 0.00 | 85 |
| MLTX-02-005-EN | Shop DWG Approval for Drainage Layout | 30 | 100% | 100% | 11-Jun-26 | 15-Jul-26 | 18-Mar-26 A | 09-May-26 A | 0.00 | 0.00 | 0.00 | 55 |
| MLTX-02-005-EN | Shop DWG Approval for Drainage Details | 30 | 100% | 100% | 11-Jun-26 | 15-Jul-26 | 18-Mar-26 A | 09-May-26 A | 0.00 | 0.00 | 0.00 | 55 |
| MLTX-02-005-EN | Shop DWG Approval for Duct Routing Layout | 30 | 100% | 100% | 11-Jun-26 | 15-Jul-26 | 18-Mar-26 A | 10-May-26 A | 0.00 | 0.00 | 0.00 | 54 |
| MLTX-02-005-EN | Shop DWG Approval for Diffusers Layout | 30 | 100% | 100% | 11-Jun-26 | 15-Jul-26 | 18-Mar-26 A | 10-May-26 A | 0.00 | 0.00 | 0.00 | 54 |
| MLTX-02-005-EN | Shop DWG Approval for Fire Fighting Layout | 30 | 100% | 100% | 11-Jun-26 | 15-Jul-26 | 24-Mar-26 A | 04-Apr-26 A | 0.00 | 0.00 | 0.00 | 85 |
| MLTX-02-005-EN | Shop DWG Approval for Water Supply Layout | 30 | 100% | 100% | 11-Jun-26 | 15-Jul-26 | 24-Mar-26 A | 04-Apr-26 A | 0.00 | 0.00 | 0.00 | 85 |
| MLTX-02-005-EN | Shop DWG Approval for Water Supply Details | 30 | 100% | 100% | 11-Jun-26 | 15-Jul-26 | 24-Mar-26 A | 04-Apr-26 A | 0.00 | 0.00 | 0.00 | 85 |
| **ELECTRICAL WORKS** | | 106 | 0% | 0% | 11-Jun-26 | 03-Aug-26 | 18-Mar-26 A | 30-Jul-26 A | 0.00 | 0.00 | 0.00 | 3 |
| MLTX-02-005-EN | Shop DWG Approval for Lighting Layout | 30 | 100% | 100% | 30-Jun-26 | 03-Aug-26 | 24-Mar-26 A | 04-Apr-26 A | 0.00 | 0.00 | 0.00 | 101 |
| MLTX-02-005-EN | Shop DWG Approval for Power Layout | 30 | 100% | 100% | 11-Jun-26 | 15-Jul-26 | 24-Mar-26 A | 04-Apr-26 A | 0.00 | 0.00 | 0.00 | 85 |
| MLTX-02-005-EN | Shop DWG Approval for Power Single Line Diagram | 30 | 100% | 100% | 11-Jun-26 | 15-Jul-26 | 18-Mar-26 A | 05-May-26 A | 0.00 | 0.00 | 0.00 | 58 |
| MLTX-02-005-EN | Shop DWG Approval for Panel Board Schedules | 30 | 100% | 100% | 11-Jun-26 | 15-Jul-26 | 16-Jul-26 A | 16-Jul-26 A | 0.00 | 0.00 | 0.00 | -1 |

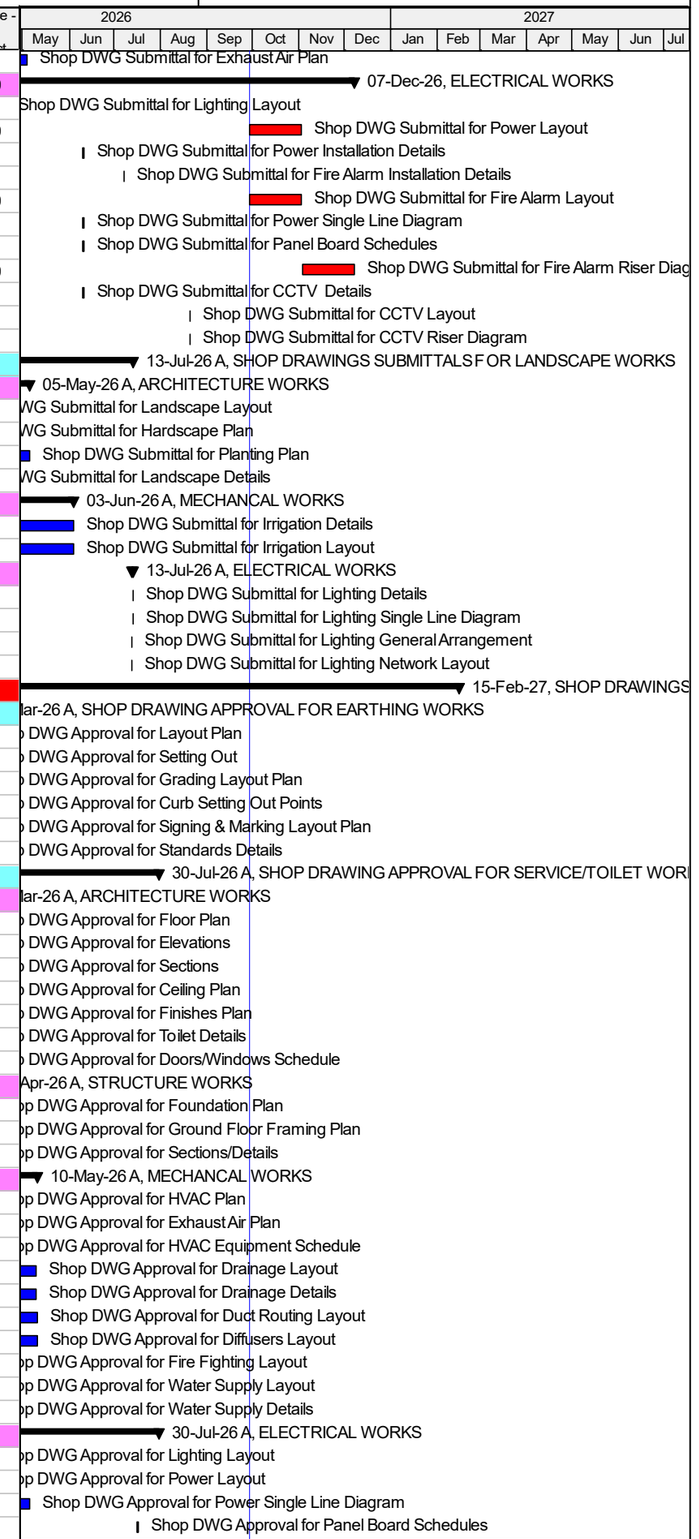


Actual Level of Effort | Actual Work | Remaining Work | Critical Remaining Work | Milestone | summary




TASK filter: All Activities

© Oracle Corporation

# MLTX-02-005 - Playground Initiative for Eastern Region (Arar-Hasa osis -Dammam)

**Updateded schedule**
**D.D 28-09-2026**

| Activity ID | Activity Name | Original Duration | Schedule % Complete | Performance % Complete | BL Project Start | BL Project Finish | Start | Finish | Planned Value Cost | Earned Value Cost | Budgeted Total Cost | Variance - BL Project |
|---|---|---|---|---|---|---|---|---|---|---|---|---|
| MLTX-02-005-EI | Shop DWG Approval for Lighting Installation Details | 30 | 100% | 100% | 11-Jun-26 | 15-Jul-26 | 24-Mar-26 A | 04-Apr-26 A | 0.00 | 0.00 | 0.00 | 85 |
| MLTX-02-005-EI | Shop DWG Approval for Power Installation Details | 30 | 100% | 100% | 11-Jun-26 | 15-Jul-26 | 24-Mar-26 A | 04-Apr-26 A | 0.00 | 0.00 | 0.00 | 85 |
| MLTX-02-005-EI | Shop DWG Approval for Cable Tray Installation Details | 30 | 100% | 100% | 11-Jun-26 | 15-Jul-26 | 18-Mar-26 A | 05-May-26 A | 0.00 | 0.00 | 0.00 | 58 |
| MLTX-02-005-EI | Shop DWG Approval for Manhole & Ductbank Details | 30 | 100% | 100% | 11-Jun-26 | 15-Jul-26 | 18-Mar-26 A | 05-May-26 A | 0.00 | 0.00 | 0.00 | 58 |
| MLTX-02-005-EI | Shop DWG Approval for Grounding Details | 30 | 100% | 100% | 11-Jun-26 | 15-Jul-26 | 24-Mar-26 A | 04-Apr-26 A | 0.00 | 0.00 | 0.00 | 85 |
| MLTX-02-005-EI | Shop DWG Approval for Fire Alarm Installation Details | 30 | 100% | 100% | 11-Jun-26 | 15-Jul-26 | 24-Mar-26 A | 04-Apr-26 A | 0.00 | 0.00 | 0.00 | 85 |
| MLTX-02-005-EI | Shop DWG Approval for Fire Alarm Layout | 30 | 100% | 100% | 11-Jun-26 | 15-Jul-26 | 24-Mar-26 A | 04-Apr-26 A | 0.00 | 0.00 | 0.00 | 85 |
| MLTX-02-005-EI | Shop DWG Approval for Lightning Protection Details | 30 | 100% | 100% | 11-Jun-26 | 15-Jul-26 | 24-Mar-26 A | 04-Apr-26 A | 0.00 | 0.00 | 0.00 | 85 |
| MLTX-02-005-EI | Shop DWG Approval for Lightning Protection System Layout | 30 | 100% | 100% | 11-Jun-26 | 15-Jul-26 | 24-Mar-26 A | 04-Apr-26 A | 0.00 | 0.00 | 0.00 | 85 |
| MLTX-02-005-EI | Shop DWG Approval for Fire Alarm Riser Diagram | 30 | 100% | 100% | 11-Jun-26 | 15-Jul-26 | 24-Mar-26 A | 04-Apr-26 A | 0.00 | 0.00 | 0.00 | 85 |
| MLTX-02-005-EI | Shop DWG Approval for CCTV Details | 30 | 100% | 100% | 11-Jun-26 | 15-Jul-26 | 30-Jul-26 A | 30-Jul-26 A | 0.00 | 0.00 | 0.00 | -13 |
| MLTX-02-005-EI | Shop DWG Approval for CCTV Layout | 30 | 100% | 100% | 11-Jun-26 | 15-Jul-26 | 30-Jul-26 A | 30-Jul-26 A | 0.00 | 0.00 | 0.00 | -13 |
| MLTX-02-005-EI | Shop DWG Approval for Telephone & Data Layout | 30 | 100% | 100% | 11-Jun-26 | 15-Jul-26 | 24-Mar-26 A | 04-Apr-26 A | 0.00 | 0.00 | 0.00 | 85 |
| MLTX-02-005-EI | Shop DWG Approval for Grounding Layout | 30 | 100% | 100% | 11-Jun-26 | 15-Jul-26 | 24-Mar-26 A | 04-Apr-26 A | 0.00 | 0.00 | 0.00 | 85 |
| MLTX-02-005-EI | Shop DWG Approval for CCTV Riser Diagram | 30 | 100% | 100% | 11-Jun-26 | 15-Jul-26 | 30-Jul-26 A | 30-Jul-26 A | 0.00 | 0.00 | 0.00 | -13 |
| MLTX-02-005-EI | Shop DWG Approval for Telephone & Data Riser Diagram | 30 | 100% | 100% | 11-Jun-26 | 15-Jul-26 | 24-Mar-26 A | 04-Apr-26 A | 0.00 | 0.00 | 0.00 | 85 |
| **SHOP DRAWINGS APPROVAL FOR PLAYGROUND WORKS** | | 180 | 0% | 0% | 29-Mar-26 | 25-Oct-26 | 14-Mar-26 A | 15-Feb-27 | 0.00 | 0.00 | 0.00 | -97 |
| **ARCHITECTURE WORKS** | | 90 | 0% | 0% | 29-Mar-26 | 09-Jun-26 | 14-Mar-26 A | 02-Nov-26 | 0.00 | 0.00 | 0.00 | -124 |
| MLTX-02-005-EI | Shop DWG Approval for Playground Plan/Layout | 15 | 100% | 100% | 29-Mar-26 | 14-Apr-26 | 15-Mar-26 A | 29-Mar-26 A | 0.00 | 0.00 | 0.00 | 14 |
| MLTX-02-005-EI | Shop DWG Approval for Furniture & Marking | 30 | 100% | 100% | 29-Mar-26 | 02-May-26 | 14-Mar-26 A | 12-May-26 A | 0.00 | 0.00 | 0.00 | -9 |
| MLTX-02-005-EI | Shop DWG Approval for Sections | 15 | 100% | 100% | 29-Mar-26 | 14-Apr-26 | 15-Mar-26 A | 29-Mar-26 A | 0.00 | 0.00 | 0.00 | 14 |
| MLTX-02-005-EI | Shop DWG Approval for Interlock Pattern Plan | 30 | 100% | 100% | 15-Apr-26 | 19-May-26 | 15-Mar-26 A | 29-Mar-26 A | 0.00 | 0.00 | 0.00 | 44 |
| MLTX-02-005-EI | Shop DWG Approval for Doors/Windows Schedule | 30 | 100% | 100% | 15-Apr-26 | 19-May-26 | 15-Mar-26 A | 29-Mar-26 A | 0.00 | 0.00 | 0.00 | 44 |
| MLTX-02-005-EI | Shop DWG Approval for Dome Internal Layout | 30 | 100% | 0% | 03-May-26 | 09-Jun-26 | 29-Sep-26 | 02-Nov-26 | 0.00 | 0.00 | 0.00 | -124 |
| **STRUCTURE WORKS** | | 45 | 0% | 0% | 20-May-26 | 27-Jun-26 | 19-Mar-26 A | 16-Jul-26 A | 0.00 | 0.00 | 0.00 | -17 |
| MLTX-02-005-EI | Shop DWG Approval for Air Dome System | 30 | 100% | 100% | 20-May-26 | 27-Jun-26 | 19-Mar-26 A | 09-May-26 A | 0.00 | 0.00 | 0.00 | 39 |
| MLTX-02-005-EI | Shop DWG Approval for Foundation of Air Dome | 30 | 100% | 100% | 20-May-26 | 27-Jun-26 | 16-Jul-26 A | 16-Jul-26 A | 0.00 | 0.00 | 0.00 | -17 |
| MLTX-02-005-EI | Shop DWG Approval for Foundation of Air Dome | 30 | 100% | 100% | 20-May-26 | 27-Jun-26 | 16-Jul-26 A | 16-Jul-26 A | 0.00 | 0.00 | 0.00 | -17 |
| MLTX-02-005-EI | Shop DWG Approval for Anchor Bolt Layout of Air Dome | 30 | 100% | 100% | 20-May-26 | 27-Jun-26 | 16-Jul-26 A | 16-Jul-26 A | 0.00 | 0.00 | 0.00 | -17 |
| **AIR DOME SYSTEM** | | 105 | 0% | 0% | 20-May-26 | 27-Jun-26 | 19-Mar-26 A | 11-Jan-27 | 0.00 | 0.00 | 0.00 | -169 |
| MLTX-02-005-EI | Shop DWG Approval for Air Dome Structural Layout | 30 | 100% | 100% | 20-May-26 | 27-Jun-26 | 19-Mar-26 A | 09-May-26 A | 0.00 | 0.00 | 0.00 | 39 |
| MLTX-02-005-EI | Shop DWG Approval for Membrane Panel Layout | 30 | 100% | 0% | 20-May-26 | 27-Jun-26 | 29-Sep-26 | 02-Nov-26 | 0.00 | 0.00 | 0.00 | -109 |
| MLTX-02-005-EI | Shop DWG Approval for Cable Tension Layout | 30 | 100% | 0% | 20-May-26 | 27-Jun-26 | 29-Sep-26 | 02-Nov-26 | 0.00 | 0.00 | 0.00 | -109 |
| MLTX-02-005-EI | Shop DWG Approval for Airlock Door Details | 30 | 100% | 0% | 20-May-26 | 27-Jun-26 | 03-Nov-26 | 07-Dec-26 | 0.00 | 0.00 | 0.00 | -139 |
| MLTX-02-005-EI | Shop DWG Approval for Emergency Exit Details | 30 | 100% | 0% | 20-May-26 | 27-Jun-26 | 08-Dec-26 | 11-Jan-27 | 0.00 | 0.00 | 0.00 | -169 |
| **SPORTS EQUIPMENT** | | 167 | 0% | 0% | 20-May-26 | 27-Jun-26 | 20-Jul-26 A | 15-Feb-27 | 0.00 | 0.00 | 0.00 | -199 |
| MLTX-02-005-EI | Shop DWG Approval for Football Turf Installation | 30 | 100% | 0% | 20-May-26 | 27-Jun-26 | 12-Jan-27 | 15-Feb-27 | 0.00 | 0.00 | 0.00 | -199 |
| MLTX-02-005-EI | Shop DWG Approval for Basketball Court Marking | 30 | 100% | 100% | 20-May-26 | 27-Jun-26 | 25-Aug-26 A | 25-Aug-26 A | 0.00 | 0.00 | 0.00 | -51 |
| MLTX-02-005-EI | Shop DWG Approval for Padel Court Structure | 30 | 100% | 100% | 20-May-26 | 27-Jun-26 | 20-Jul-26 A | 20-Jul-26 A | 0.00 | 0.00 | 0.00 | -20 |
| **MECHANCAL WORKS** | | 60 | 0% | 0% | 20-May-26 | 01-Aug-26 | 19-Mar-26 A | 04-May-26 A | 0.00 | 0.00 | 0.00 | 73 |
| MLTX-02-005-EI | Shop DWG Approval for HVAC Plan | 30 | 100% | 100% | 20-May-26 | 27-Jun-26 | 19-Mar-26 A | 04-May-26 A | 0.00 | 0.00 | 0.00 | 43 |
| MLTX-02-005-EI | Shop DWG Approval for Exhaust Air Plan | 30 | 100% | 100% | 28-Jun-26 | 01-Aug-26 | 19-Mar-26 A | 04-May-26 A | 0.00 | 0.00 | 0.00 | 73 |
| **ELECTRICAL WORKS** | | 167 | 0% | 0% | 20-May-26 | 25-Oct-26 | 13-Jun-26 A | 27-Jan-27 | 0.00 | 0.00 | 0.00 | -81 |
| MLTX-02-005-EI | Shop DWG Approval for Lighting Layout | 15 | 100% | 0% | 20-May-26 | 09-Jun-26 | 29-Sep-26 | 15-Oct-26 | 0.00 | 0.00 | 0.00 | -109 |
| MLTX-02-005-EI | Shop DWG Approval for Power Layout | 30 | 100% | 0% | 02-Aug-26 | 05-Sep-26 | 08-Dec-26 | 11-Jan-27 | 0.00 | 0.00 | 0.00 | -109 |
| MLTX-02-005-EI | Shop DWG Approval for Power Installation Details | 14 | 100% | 0% | 06-Sep-26 | 21-Sep-26 | 12-Jan-27 | 27-Jan-27 | 0.00 | 0.00 | 0.00 | -109 |
| MLTX-02-005-EI | Shop DWG Approval for Power Single Line Diagram | 30 | 100% | 100% | 20-May-26 | 27-Jun-26 | 16-Jul-26 A | 16-Jul-26 A | 0.00 | 0.00 | 0.00 | -17 |
| MLTX-02-005-EI | Shop DWG Approval for Panel Board Schedules | 20 | 100% | 100% | 20-May-26 | 15-Jun-26 | 13-Jun-26 A | 13-Jun-26 A | 0.00 | 0.00 | 0.00 | 2 |
| MLTX-02-005-EI | Shop DWG Approval for CCTV Details | 25 | 20% | 100% | 22-Sep-26 | 21-Oct-26 | 25-Aug-26 A | 25-Aug-26 A | 0.00 | 0.00 | 0.00 | 48 |
| MLTX-02-005-EI | Shop DWG Approval for CCTV Layout | 3 | 0% | 100% | 22-Oct-26 | 25-Oct-26 | 25-Aug-26 A | 25-Aug-26 A | 0.00 | 0.00 | 0.00 | 51 |
| MLTX-02-005-EI | Shop DWG Approval for CCTV Riser Diagram | 30 | 100% | 100% | 20-May-26 | 27-Jun-26 | 25-Aug-26 A | 25-Aug-26 A | 0.00 | 0.00 | 0.00 | -51 |
| **SHOP DRAWINGS APPROVAL FOR LANDSCAPE WORKS** | | 41 | 0% | 0% | 29-Mar-26 | 01-Aug-26 | 15-Mar-26 A | 16-Jul-26 A | 0.00 | 0.00 | 0.00 | 13 |
| **ARCHITECTURE WORKS** | | 36 | 0% | 0% | 29-Mar-26 | 09-May-26 | 15-Mar-26 A | 19-May-26 A | 0.00 | 0.00 | 0.00 | -9 |
| MLTX-02-005-EI | Shop DWG Approval for Landscape Layout | 21 | 100% | 100% | 15-Apr-26 | 09-May-26 | 15-Mar-26 A | 29-Mar-26 A | 0.00 | 0.00 | 0.00 | 35 |
| MLTX-02-005-EI | Shop DWG Approval for Hardscape Plan | 21 | 100% | 100% | 05-Apr-26 | 28-Apr-26 | 15-Mar-26 A | 29-Mar-26 A | 0.00 | 0.00 | 0.00 | 26 |
| MLTX-02-005-EI | Shop DWG Approval for Planting Plan | 15 | 100% | 100% | 15-Apr-26 | 02-May-26 | 19-Mar-26 A | 19-May-26 A | 0.00 | 0.00 | 0.00 | -15 |
| MLTX-02-005-EI | Shop DWG Approval for Landscape Details | 21 | 100% | 100% | 29-Mar-26 | 21-Apr-26 | 15-Mar-26 A | 29-Mar-26 A | 0.00 | 0.00 | 0.00 | 20 |
| **MECHANCAL WORKS** | | 30 | 0% | 0% | 15-Apr-26 | 19-May-26 | 07-Jul-26 A | 07-Jul-26 A | 0.00 | 0.00 | 0.00 | -39 |
| MLTX-02-005-EI | Shop DWG Approval for Irrigation Details | 30 | 100% | 100% | 15-Apr-26 | 19-May-26 | 07-Jul-26 A | 07-Jul-26 A | 0.00 | 0.00 | 0.00 | -39 |
| MLTX-02-005-EI | Shop DWG Approval for Irrigation Layout | 30 | 100% | 100% | 15-Apr-26 | 19-May-26 | 07-Jul-26 A | 07-Jul-26 A | 0.00 | 0.00 | 0.00 | -39 |
| **ELECTRICAL WORKS** | | 30 | 0% | 0% | 15-Apr-26 | 01-Aug-26 | 16-Jul-26 A | 16-Jul-26 A | 0.00 | 0.00 | 0.00 | 13 |
| MLTX-02-005-EI | Shop DWG Approval for Lighting Details | 30 | 100% | 100% | 15-Apr-26 | 19-May-26 | 16-Jul-26 A | 16-Jul-26 A | 0.00 | 0.00 | 0.00 | -47 |
| MLTX-02-005-EI | Shop DWG Approval for Lighting Single Line Diagram | 30 | 100% | 100% | 28-Jun-26 | 01-Aug-26 | 16-Jul-26 A | 16-Jul-26 A | 0.00 | 0.00 | 0.00 | 13 |
| MLTX-02-005-EI | Shop DWG Approval for Lighting General Arrangement | 30 | 100% | 100% | 15-Apr-26 | 19-May-26 | 16-Jul-26 A | 16-Jul-26 A | 0.00 | 0.00 | 0.00 | -47 |

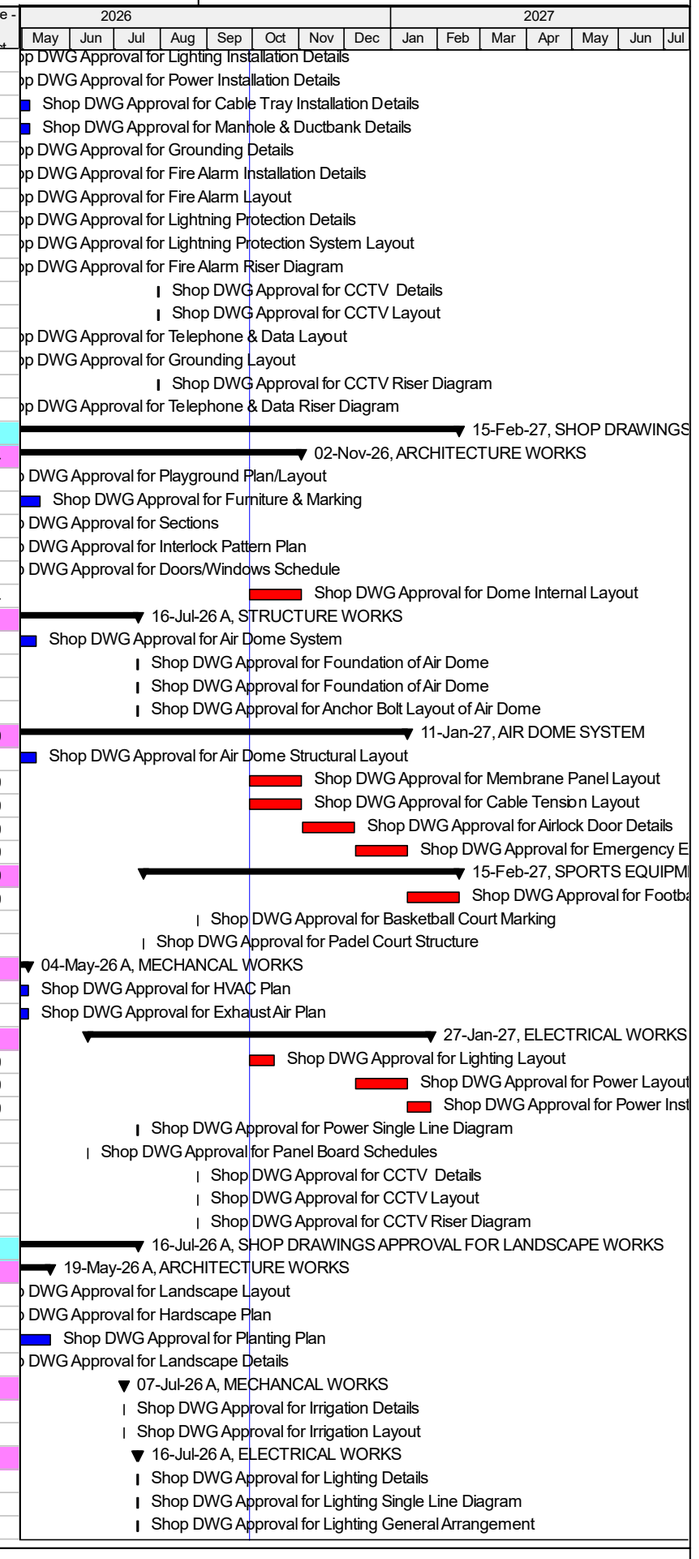






© Oracle Corporation

# MLTX-02-005 - Playground Initiative for Eastern Region (Arar-Hasa osis -Dammam)

**Updateded schedule**
**D.D 28-09-2026**

| Activity ID | Activity Name | Original Duration | Schedule % Complete | Performance % Complete | BL Project Start | BL Project Finish | Start | Finish | Planned Value Cost | Earned Value Cost | Budgeted Total Cost | Variance - BL Project |
|---|---|---|---|---|---|---|---|---|---|---|---|---|
| MLTX-02-005-EN | Shop DWG Approval for Lighting Network Layout | 30 | 100% | 100% | 15-Apr-26 | 19-May-26 | 16-Jul-26 A | 16-Jul-26 A | 0.00 | 0.00 | 0.00 | -47 |
| **METHOD STATEMENTS** | | 97 | 0% | 0% | 07-Mar-26 | 20-Jul-26 | 07-Mar-26 A | 12-Sep-26 A | 0.00 | 0.00 | 0.00 | -46 |
| **METHOD STATEMENT SUBMITTAL** | | 80 | 0% | 0% | 07-Mar-26 | 14-Jun-26 | 07-Mar-26 A | 04-Jun-26 A | 0.00 | 0.00 | 0.00 | 8 |
| **CIVIL WORKS** | | 30 | 0% | 0% | 07-Mar-26 | 13-Apr-26 | 09-Mar-26 A | 14-Mar-26 A | 0.00 | 0.00 | 0.00 | 23 |
| MLTX-02-005-EN-4 | Preparation & Submission of Method Statement for | 15 | 100% | 100% | 07-Mar-26 | 26-Mar-26 | 09-Mar-26 A | 14-Mar-26 A | 0.00 | 0.00 | 0.00 | 8 |
| MLTX-02-005-EN-4 | Preparation & Submission of Method Statement for Concrete | 30 | 100% | 100% | 07-Mar-26 | 13-Apr-26 | 09-Mar-26 A | 14-Mar-26 A | 0.00 | 0.00 | 0.00 | 23 |
| MLTX-02-005-EN-4 | Preparation & Submission of Method Statement for | 21 | 100% | 100% | 07-Mar-26 | 02-Apr-26 | 09-Mar-26 A | 14-Mar-26 A | 0.00 | 0.00 | 0.00 | 14 |
| **ARCHITECTURE WORKS** | | 30 | 0% | 0% | 07-Mar-26 | 13-Apr-26 | 07-Mar-26 A | 02-Jun-26 A | 0.00 | 0.00 | 0.00 | -40 |
| MLTX-02-005-EN-4 | Preparation & Submission of Method Statement for Plastering | 15 | 100% | 100% | 07-Mar-26 | 26-Mar-26 | 09-Mar-26 A | 14-Mar-26 A | 0.00 | 0.00 | 0.00 | 8 |
| MLTX-02-005-EN-4 | Preparation & Submission of Method Statement for | 30 | 100% | 100% | 07-Mar-26 | 13-Apr-26 | 07-Mar-26 A | 11-May-26 A | 0.00 | 0.00 | 0.00 | -24 |
| MLTX-02-005-EN-4 | Preparation & Submission of Method Statement for Tilling | 30 | 100% | 100% | 07-Mar-26 | 13-Apr-26 | 07-Mar-26 A | 17-May-26 A | 0.00 | 0.00 | 0.00 | -29 |
| MLTX-02-005-EN-4 | Preparation & Submission of Method Statement for | 30 | 100% | 100% | 07-Mar-26 | 13-Apr-26 | 07-Mar-26 A | 02-Jun-26 A | 0.00 | 0.00 | 0.00 | -40 |
| MLTX-02-005-EN-4 | Preparation & Submission of Method Statement for | 30 | 100% | 100% | 07-Mar-26 | 13-Apr-26 | 07-Mar-26 A | 02-Jun-26 A | 0.00 | 0.00 | 0.00 | -40 |
| MLTX-02-005-EN-4 | Preparation & Submission of Method Statement for | 30 | 100% | 100% | 07-Mar-26 | 13-Apr-26 | 07-Mar-26 A | 02-May-26 A | 0.00 | 0.00 | 0.00 | -16 |
| MLTX-02-005-EN-4 | Preparation & Submission of Method Statement for Parking | 30 | 100% | 100% | 07-Mar-26 | 13-Apr-26 | 07-Mar-26 A | 24-May-26 A | 0.00 | 0.00 | 0.00 | -35 |
| MLTX-02-005-EN-4 | Preparation & Submission of Method Statement for Soft | 30 | 100% | 100% | 07-Mar-26 | 13-Apr-26 | 07-Mar-26 A | 02-Jun-26 A | 0.00 | 0.00 | 0.00 | -40 |
| MLTX-02-005-EN-4 | Preparation & Submission of Method Statement for Fence | 30 | 100% | 100% | 07-Mar-26 | 13-Apr-26 | 07-Mar-26 A | 02-Jun-26 A | 0.00 | 0.00 | 0.00 | -40 |
| MLTX-02-005-EN-4 | Preparation & Submission of Method Statement for Air Dome | 30 | 100% | 100% | 07-Mar-26 | 13-Apr-26 | 07-Mar-26 A | 02-Jun-26 A | 0.00 | 0.00 | 0.00 | -40 |
| MLTX-02-005-EN-4 | Preparation & Submission of Method Statement for Metal | 30 | 100% | 100% | 07-Mar-26 | 13-Apr-26 | 07-Mar-26 A | 02-Jun-26 A | 0.00 | 0.00 | 0.00 | -40 |
| MLTX-02-005-EN-4 | Preparation & Submission of Method Statement for Partitions | 30 | 100% | 100% | 07-Mar-26 | 13-Apr-26 | 07-Mar-26 A | 02-Jun-26 A | 0.00 | 0.00 | 0.00 | -40 |
| MLTX-02-005-EN-4 | Preparation & Submission of Method Statement for Gypsum | 30 | 100% | 100% | 07-Mar-26 | 13-Apr-26 | 07-Mar-26 A | 02-Jun-26 A | 0.00 | 0.00 | 0.00 | -40 |
| **MECHANICAL WORKS** | | 45 | 0% | 0% | 28-Mar-26 | 18-May-26 | 12-Mar-26 A | 04-Jun-26 A | 0.00 | 0.00 | 0.00 | -12 |
| MLTX-02-005-EN-4 | Preparation & Submission of Method Statement for | 30 | 100% | 100% | 28-Mar-26 | 30-Apr-26 | 12-Mar-26 A | 02-May-26 A | 0.00 | 0.00 | 0.00 | -1 |
| MLTX-02-005-EN-4 | Preparation & Submission of Method Statement for Water | 30 | 100% | 100% | 14-Apr-26 | 18-May-26 | 12-Mar-26 A | 02-May-26 A | 0.00 | 0.00 | 0.00 | 14 |
| MLTX-02-005-EN-4 | Preparation & Submission of Method Statement for Fire | 30 | 100% | 100% | 04-Apr-26 | 07-May-26 | 12-Mar-26 A | 04-Jun-26 A | 0.00 | 0.00 | 0.00 | -21 |
| MLTX-02-005-EN-4 | Preparation & Submission of Method Statement for Irrigation | 15 | 100% | 100% | 28-Mar-26 | 13-Apr-26 | 12-Mar-26 A | 04-Jun-26 A | 0.00 | 0.00 | 0.00 | -42 |
| MLTX-02-005-EN-4 | Preparation & Submission of Method Statement for HVAC | 30 | 100% | 100% | 14-Apr-26 | 18-May-26 | 12-Mar-26 A | 04-Jun-26 A | 0.00 | 0.00 | 0.00 | -12 |
| **ELECTRICAL WORKS** | | 50 | 0% | 0% | 14-Apr-26 | 14-Jun-26 | 12-Mar-26 A | 11-May-26 A | 0.00 | 0.00 | 0.00 | 26 |
| MLTX-02-005-EN-4 | Preparation & Submission of Method Statement for | 30 | 100% | 100% | 14-Apr-26 | 18-May-26 | 12-Mar-26 A | 11-May-26 A | 0.00 | 0.00 | 0.00 | 6 |
| MLTX-02-005-EN-4 | Preparation & Submission of Method Statement for CCTV | 30 | 100% | 100% | 07-May-26 | 14-Jun-26 | 12-Mar-26 A | 11-May-26 A | 0.00 | 0.00 | 0.00 | 26 |
| MLTX-02-005-EN-4 | Preparation & Submission of Method Statement for Lighting | 30 | 100% | 100% | 14-Apr-26 | 18-May-26 | 12-Mar-26 A | 11-May-26 A | 0.00 | 0.00 | 0.00 | 6 |
| MLTX-02-005-EN-4 | Preparation & Submission of Method Statement for | 30 | 100% | 100% | 14-Apr-26 | 18-May-26 | 12-Mar-26 A | 06-May-26 A | 0.00 | 0.00 | 0.00 | 10 |
| MLTX-02-005-EN-4 | Preparation & Submission of Method Statement for Panel | 30 | 100% | 100% | 14-Apr-26 | 18-May-26 | 12-Mar-26 A | 11-May-26 A | 0.00 | 0.00 | 0.00 | 6 |
| MLTX-02-005-EN-4 | Preparation & Submission of Method Statement for Electrical | 30 | 100% | 100% | 14-Apr-26 | 18-May-26 | 12-Mar-26 A | 11-May-26 A | 0.00 | 0.00 | 0.00 | 6 |
| MLTX-02-005-EN-4 | Preparation & Submission of Method Statement for Lighting | 30 | 100% | 100% | 14-Apr-26 | 18-May-26 | 12-Mar-26 A | 11-May-26 A | 0.00 | 0.00 | 0.00 | 6 |
| **METHOD STATEMENT APPROVAL** | | 82 | 0% | 0% | 28-Mar-26 | 20-Jul-26 | 12-Mar-26 A | 12-Sep-26 A | 0.00 | 0.00 | 0.00 | -46 |
| **CIVIL WORKS** | | 45 | 0% | 0% | 28-Mar-26 | 18-May-26 | 12-Mar-26 A | 30-Apr-26 A | 0.00 | 0.00 | 0.00 | 15 |
| MLTX-02-005-EN-4 | Approval of Method Statement for Earthwork | 15 | 100% | 100% | 28-Mar-26 | 13-Apr-26 | 12-Mar-26 A | 30-Apr-26 A | 0.00 | 0.00 | 0.00 | -15 |
| MLTX-02-005-EN-4 | Approval of Method Statement for Concrete Works | 30 | 100% | 100% | 14-Apr-26 | 18-May-26 | 12-Mar-26 A | 30-Apr-26 A | 0.00 | 0.00 | 0.00 | 15 |
| MLTX-02-005-EN-4 | Approval of Method Statement for Waterproofing | 21 | 100% | 100% | 04-Apr-26 | 27-Apr-26 | 12-Mar-26 A | 30-Apr-26 A | 0.00 | 0.00 | 0.00 | -3 |
| **ARCHITECTURE WORKS** | | 80 | 0% | 0% | 28-Mar-26 | 18-May-26 | 12-Mar-26 A | 12-Sep-26 A | 0.00 | 0.00 | 0.00 | -97 |
| MLTX-02-005-EN-4 | Approval of Method Statement for Plastering Works | 30 | 100% | 100% | 28-Mar-26 | 30-Apr-26 | 12-Mar-26 A | 30-Apr-26 A | 0.00 | 0.00 | 0.00 | 0 |
| MLTX-02-005-EN-4 | Approval of Method Statement for Masonary Works | 30 | 100% | 100% | 14-Apr-26 | 18-May-26 | 12-Mar-26 A | 24-May-26 A | 0.00 | 0.00 | 0.00 | -5 |
| MLTX-02-005-EN-4 | Approval of Method Statement for Tilling Works | 30 | 100% | 100% | 14-Apr-26 | 18-May-26 | 12-Mar-26 A | 24-May-26 A | 0.00 | 0.00 | 0.00 | -5 |
| MLTX-02-005-EN-4 | Approval of Method Statement for Seats/Benches Works | 30 | 100% | 100% | 14-Apr-26 | 18-May-26 | 12-Sep-26 A | 12-Sep-26 A | 0.00 | 0.00 | 0.00 | -97 |
| MLTX-02-005-EN-4 | Approval of Method Statement for Doors/Windows Works | 30 | 100% | 100% | 14-Apr-26 | 18-May-26 | 12-Sep-26 A | 12-Sep-26 A | 0.00 | 0.00 | 0.00 | -97 |
| MLTX-02-005-EN-4 | Approval of Method Statement for Interlock/Curbstone Works | 30 | 100% | 100% | 14-Apr-26 | 18-May-26 | 12-Mar-26 A | 05-May-26 A | 0.00 | 0.00 | 0.00 | 11 |
| MLTX-02-005-EN-4 | Approval of Method Statement for Parking Works | 30 | 100% | 100% | 14-Apr-26 | 18-May-26 | 20-May-26 A | 20-May-26 A | 0.00 | 0.00 | 0.00 | -2 |
| MLTX-02-005-EN-4 | Approval of Method Statement for Soft Scape Works | 30 | 100% | 100% | 14-Apr-26 | 18-May-26 | 19-Jul-26 A | 19-Jul-26 A | 0.00 | 0.00 | 0.00 | -50 |
| MLTX-02-005-EN-4 | Approval of Method Statement for Fence Works | 20 | 100% | 100% | 14-Apr-26 | 06-May-26 | 19-Jul-26 A | 19-Jul-26 A | 0.00 | 0.00 | 0.00 | -60 |
| MLTX-02-005-EN-4 | Approval of Method Statement for Air Dome Works | 30 | 100% | 100% | 14-Apr-26 | 18-May-26 | 12-Sep-26 A | 12-Sep-26 A | 0.00 | 0.00 | 0.00 | -97 |
| MLTX-02-005-EN-4 | Approval of Method Statement for Partitions Works | 30 | 100% | 100% | 14-Apr-26 | 18-May-26 | 29-Jun-26 A | 29-Jun-26 A | 0.00 | 0.00 | 0.00 | -33 |
| MLTX-02-005-EN-4 | Approval of Method Statement for Gypsum Board Works | 30 | 100% | 100% | 14-Apr-26 | 18-May-26 | 20-Aug-26 A | 20-Aug-26 A | 0.00 | 0.00 | 0.00 | -78 |
| **MECHANICAL WORKS** | | 63 | 0% | 0% | 14-Apr-26 | 25-Jun-26 | 14-Jun-26 A | 26-Aug-26 A | 0.00 | 0.00 | 0.00 | -53 |
| MLTX-02-005-EN-4 | Approval of Method Statement for Sewage/Drainage System | 30 | 100% | 100% | 02-May-26 | 08-Jun-26 | 14-Jun-26 A | 14-Jun-26 A | 0.00 | 0.00 | 0.00 | -5 |
| MLTX-02-005-EN-4 | Approval of Method Statement for Water Supply System | 30 | 100% | 100% | 19-May-26 | 25-Jun-26 | 14-Jun-26 A | 14-Jun-26 A | 0.00 | 0.00 | 0.00 | 10 |
| MLTX-02-005-EN-4 | Approval of Method Statement for Fire Fighting System | 30 | 100% | 100% | 09-May-26 | 15-Jun-26 | 26-Aug-26 A | 26-Aug-26 A | 0.00 | 0.00 | 0.00 | -62 |
| MLTX-02-005-EN-4 | Approval of Method Statement for Irrigation System | 15 | 100% | 100% | 14-Apr-26 | 30-Apr-26 | 14-Jun-26 A | 14-Jun-26 A | 0.00 | 0.00 | 0.00 | -35 |
| MLTX-02-005-EN-4 | Approval of Method Statement for HVAC System | 30 | 100% | 100% | 19-May-26 | 25-Jun-26 | 14-Jul-26 A | 22-Jul-26 A | 0.00 | 0.00 | 0.00 | -23 |
| **ELECTRICAL WORKS** | | 80 | 0% | 0% | 19-May-26 | 20-Jul-26 | 06-Jun-26 A | 14-Jun-26 A | 0.00 | 0.00 | 0.00 | 31 |
| MLTX-02-005-EN-4 | Approval of Method Statement for Electrical Conduits/Pulling | 30 | 100% | 100% | 19-May-26 | 25-Jun-26 | 06-Jun-26 A | 06-Jun-26 A | 0.00 | 0.00 | 0.00 | 17 |
| MLTX-02-005-EN-4 | Approval of Method Statement for Lighting Poles Installation | 30 | 100% | 100% | 19-May-26 | 25-Jun-26 | 14-Jun-26 A | 14-Jun-26 A | 0.00 | 0.00 | 0.00 | 10 |
| MLTX-02-005-EN-4 | Approval of Method Statement for Telecommunication & Data | 30 | 100% | 100% | 19-May-26 | 25-Jun-26 | 14-Jun-26 A | 14-Jun-26 A | 0.00 | 0.00 | 0.00 | 10 |
| MLTX-02-005-EN-4 | Approval of Method Statement for CCTV System | 30 | 100% | 100% | 15-Jun-26 | 19-Jul-26 | 14-Jun-26 A | 14-Jun-26 A | 0.00 | 0.00 | 0.00 | 30 |

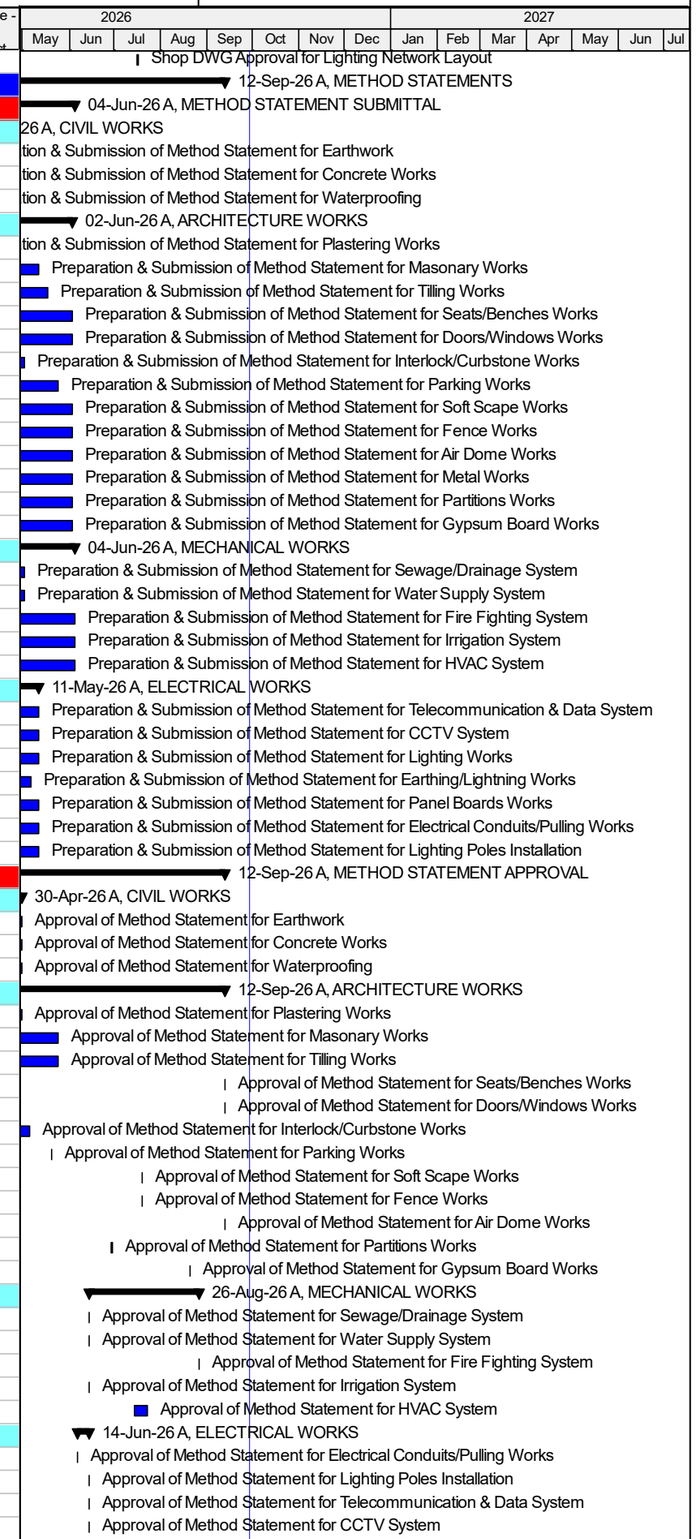




© Oracle Corporation

# MLTX-02-005 - Playground Initiative for Eastern Region (Arar-Hasa osis -Dammam)

**Updateded schedule**
**D.D 28-09-2026**

| Activity ID | Activity Name | Original Duration | Schedule % Complete | Performance % Complete | BL Project Start | BL Project Finish | Start | Finish | Planned Value Cost | Earned Value Cost | Budgeted Total Cost | Variance - BL Project |
|---|---|---|---|---|---|---|---|---|---|---|---|---|
| MLTX-02-005-EN-4 | Approval of Method Statement for Lighting Works | 30 | 100% | 100% | 10-Jun-26 | 14-Jul-26 | 14-Jun-26 A | 14-Jun-26 A | 0.00 | 0.00 | 0.00 | 26 |
| MLTX-02-005-EN-4 | Approval of Method Statement for Earthing/Lightning Works | 30 | 100% | 100% | 19-May-26 | 25-Jun-26 | 14-Jun-26 A | 14-Jun-26 A | 0.00 | 0.00 | 0.00 | 10 |
| MLTX-02-005-EN-4 | Approval of Method Statement for Panel Boards Works | 30 | 100% | 100% | 16-Jun-26 | 20-Jul-26 | 14-Jun-26 A | 14-Jun-26 A | 0.00 | 0.00 | 0.00 | 31 |
| **PRE-QUALIFICATION & MATERIAL** | | 105 | 0% | 0% | 07-Mar-26 | 13-Jul-26 | 07-Mar-26 A | 12-Sep-26 A | 0.00 | 0.00 | 0.00 | -52 |
| **PRE-QUALIFICATION** | | 45 | 0% | 0% | 07-Mar-26 | 30-Apr-26 | 07-Mar-26 A | 07-Jun-26 A | 0.00 | 0.00 | 0.00 | -29 |
| **TOILET/SERVICE WORKS** | | 45 | 0% | 0% | 07-Mar-26 | 30-Apr-26 | 07-Mar-26 A | 07-Jun-26 A | 0.00 | 0.00 | 0.00 | -29 |
| **STEEL REINFORCEMENT** | | 30 | 0% | 0% | 07-Mar-26 | 13-Apr-26 | 09-Mar-26 A | 19-Mar-26 A | 0.00 | 0.00 | 0.00 | 18 |
| MLTX-02-005-EN | Pre-Qualification Submittal for Steel Reinforcement | 15 | 100% | 100% | 07-Mar-26 | 26-Mar-26 | 09-Mar-26 A | 11-Mar-26 A | 0.00 | 0.00 | 0.00 | 10 |
| MLTX-02-005-EN | Pre-Qualification Approval for Steel Reinforcement | 15 | 100% | 100% | 28-Mar-26 | 13-Apr-26 | 12-Mar-26 A | 19-Mar-26 A | 0.00 | 0.00 | 0.00 | 18 |
| **READY MIX CONCRETE** | | 30 | 0% | 0% | 07-Mar-26 | 13-Apr-26 | 09-Mar-26 A | 19-Mar-26 A | 0.00 | 0.00 | 0.00 | 18 |
| MLTX-02-005-EN | Pre-Qualification Submittal for Ready Mixed Concrete | 15 | 100% | 100% | 07-Mar-26 | 26-Mar-26 | 09-Mar-26 A | 11-Mar-26 A | 0.00 | 0.00 | 0.00 | 10 |
| MLTX-02-005-EN | Pre-Qualification Approval of Ready Mixed Concrete | 15 | 100% | 100% | 28-Mar-26 | 13-Apr-26 | 12-Mar-26 A | 19-Mar-26 A | 0.00 | 0.00 | 0.00 | 18 |
| **CONCRETE BLOCKS** | | 30 | 0% | 0% | 07-Mar-26 | 13-Apr-26 | 09-Mar-26 A | 19-Mar-26 A | 0.00 | 0.00 | 0.00 | 18 |
| MLTX-02-005-EN | Pre-Qualification Submittal for Concrete Blocks | 15 | 100% | 100% | 07-Mar-26 | 26-Mar-26 | 09-Mar-26 A | 11-Mar-26 A | 0.00 | 0.00 | 0.00 | 10 |
| MLTX-02-005-EN | Pre-Qualification Approval for Concrete Blocks | 15 | 100% | 100% | 28-Mar-26 | 13-Apr-26 | 12-Mar-26 A | 19-Mar-26 A | 0.00 | 0.00 | 0.00 | 18 |
| **WATER PROOFING** | | 45 | 0% | 0% | 07-Mar-26 | 30-Apr-26 | 09-Mar-26 A | 19-Mar-26 A | 0.00 | 0.00 | 0.00 | 33 |
| MLTX-02-005-EN | Pre-Qualification Submittal for Water Proofing | 15 | 100% | 100% | 07-Mar-26 | 26-Mar-26 | 09-Mar-26 A | 11-Mar-26 A | 0.00 | 0.00 | 0.00 | 10 |
| MLTX-02-005-EN | Pre-Qualification Approval for Water Proofing | 30 | 100% | 100% | 28-Mar-26 | 30-Apr-26 | 12-Mar-26 A | 19-Mar-26 A | 0.00 | 0.00 | 0.00 | 33 |
| **FLOOR/WALL TILES** | | 30 | 0% | 0% | 07-Mar-26 | 13-Apr-26 | 07-Mar-26 A | 07-Apr-26 A | 0.00 | 0.00 | 0.00 | 5 |
| MLTX-02-005-EN | Pre-Qualification Submittal for Tilling Materials | 15 | 100% | 100% | 07-Mar-26 | 26-Mar-26 | 07-Mar-26 A | 29-Mar-26 A | 0.00 | 0.00 | 0.00 | -2 |
| MLTX-02-005-EN | Pre-Qualification Approval for Tailling Material | 15 | 100% | 100% | 28-Mar-26 | 13-Apr-26 | 10-Mar-26 A | 07-Apr-26 A | 0.00 | 0.00 | 0.00 | 5 |
| **SUSPENDED CEILING** | | 30 | 0% | 0% | 07-Mar-26 | 13-Apr-26 | 09-Mar-26 A | 19-Mar-26 A | 0.00 | 0.00 | 0.00 | 18 |
| MLTX-02-005-EN | Pre-Qualification Submittal for Suspend Ceiling | 15 | 100% | 100% | 07-Mar-26 | 26-Mar-26 | 09-Mar-26 A | 11-Mar-26 A | 0.00 | 0.00 | 0.00 | 10 |
| MLTX-02-005-EN | Pre-Qualification Approval for Suspend Ceiling | 15 | 100% | 100% | 28-Mar-26 | 13-Apr-26 | 12-Mar-26 A | 19-Mar-26 A | 0.00 | 0.00 | 0.00 | 18 |
| **DOORS/WINDOWS** | | 30 | 0% | 0% | 07-Mar-26 | 13-Apr-26 | 09-Mar-26 A | 19-Mar-26 A | 0.00 | 0.00 | 0.00 | 18 |
| MLTX-02-005-EN | Pre-Qualification Submittal for Doors/Windows | 15 | 100% | 100% | 07-Mar-26 | 26-Mar-26 | 09-Mar-26 A | 11-Mar-26 A | 0.00 | 0.00 | 0.00 | 10 |
| MLTX-02-005-EN | Pre-Qualification Approval for Doors/Windows | 15 | 100% | 100% | 28-Mar-26 | 13-Apr-26 | 12-Mar-26 A | 19-Mar-26 A | 0.00 | 0.00 | 0.00 | 18 |
| **FURNITURES** | | 30 | 0% | 0% | 07-Mar-26 | 13-Apr-26 | 07-Mar-26 A | 07-Apr-26 A | 0.00 | 0.00 | 0.00 | 5 |
| MLTX-02-005-EN | Pre-Qualification Submittal for Furnitures | 15 | 100% | 100% | 07-Mar-26 | 26-Mar-26 | 07-Mar-26 A | 04-Apr-26 A | 0.00 | 0.00 | 0.00 | -7 |
| MLTX-02-005-EN | Pre-Qualification Approval for Furnitures | 15 | 100% | 100% | 28-Mar-26 | 13-Apr-26 | 10-Mar-26 A | 07-Apr-26 A | 0.00 | 0.00 | 0.00 | 5 |
| **SANITARY FIXTURES** | | 30 | 0% | 0% | 07-Mar-26 | 13-Apr-26 | 07-Mar-26 A | 09-Apr-26 A | 0.00 | 0.00 | 0.00 | 3 |
| MLTX-02-005-EN | Pre-Qualification Submittal for Sanitary Fixtures | 15 | 100% | 100% | 07-Mar-26 | 26-Mar-26 | 07-Mar-26 A | 05-Apr-26 A | 0.00 | 0.00 | 0.00 | -8 |
| MLTX-02-005-EN | Pre-Qualification Approval for Sanitary Fixtures | 15 | 100% | 100% | 28-Mar-26 | 13-Apr-26 | 10-Mar-26 A | 09-Apr-26 A | 0.00 | 0.00 | 0.00 | 3 |
| **WATER SUPPLY PIPES** | | 30 | 0% | 0% | 07-Mar-26 | 13-Apr-26 | 07-Mar-26 A | 29-Mar-26 A | 0.00 | 0.00 | 0.00 | 13 |
| MLTX-02-005-EN | Pre-Qualification Submittal for Water Supply Pipes | 15 | 100% | 100% | 07-Mar-26 | 26-Mar-26 | 07-Mar-26 A | 23-Mar-26 A | 0.00 | 0.00 | 0.00 | 3 |
| MLTX-02-005-EN | Pre-Qualification Approval for Water Supply Pipes | 15 | 100% | 100% | 28-Mar-26 | 13-Apr-26 | 10-Mar-26 A | 29-Mar-26 A | 0.00 | 0.00 | 0.00 | 13 |
| **SEWAGE/DRAINAGE PIPES** | | 30 | 0% | 0% | 07-Mar-26 | 13-Apr-26 | 07-Mar-26 A | 29-Mar-26 A | 0.00 | 0.00 | 0.00 | 13 |
| MLTX-02-005-EN | Pre-Qualification Submittal for Sewage/Drainage Pipes | 15 | 100% | 100% | 07-Mar-26 | 26-Mar-26 | 07-Mar-26 A | 23-Mar-26 A | 0.00 | 0.00 | 0.00 | 3 |
| MLTX-02-005-EN | Pre-Qualification Approval for Sewage/Drainage Pipes | 15 | 100% | 100% | 28-Mar-26 | 13-Apr-26 | 10-Mar-26 A | 29-Mar-26 A | 0.00 | 0.00 | 0.00 | 13 |
| **PACKAGE AC UNITS** | | 30 | 0% | 0% | 28-Mar-26 | 30-Apr-26 | 10-Mar-26 A | 07-Apr-26 A | 0.00 | 0.00 | 0.00 | 20 |
| MLTX-02-005-EN | Pre-Qualification Submittal for Package AC Units | 15 | 100% | 100% | 28-Mar-26 | 13-Apr-26 | 10-Mar-26 A | 01-Apr-26 A | 0.00 | 0.00 | 0.00 | 10 |
| MLTX-02-005-EN | Pre-Qualification Approval for Package AC Units | 15 | 100% | 100% | 14-Apr-26 | 30-Apr-26 | 14-Mar-26 A | 07-Apr-26 A | 0.00 | 0.00 | 0.00 | 20 |
| **AIR DIFUSSERS/GRILLS** | | 30 | 0% | 0% | 28-Mar-26 | 30-Apr-26 | 10-Mar-26 A | 07-Jun-26 A | 0.00 | 0.00 | 0.00 | -29 |
| MLTX-02-005-EN | Pre-Qualification Submittal for Air Diffusers/Grills | 15 | 100% | 100% | 28-Mar-26 | 13-Apr-26 | 10-Mar-26 A | 25-May-26 A | 0.00 | 0.00 | 0.00 | -36 |
| MLTX-02-005-EN | Pre-Qualification Approval for Air Diffusers/Grills | 15 | 100% | 100% | 14-Apr-26 | 30-Apr-26 | 14-Mar-26 A | 07-Jun-26 A | 0.00 | 0.00 | 0.00 | -29 |
| **GALVANIZED DUCTS** | | 30 | 0% | 0% | 28-Mar-26 | 30-Apr-26 | 10-Mar-26 A | 30-Apr-26 A | 0.00 | 0.00 | 0.00 | 0 |
| MLTX-02-005-EN | Pre-Qualification Submittal for Galvanized Ducts | 15 | 100% | 100% | 28-Mar-26 | 13-Apr-26 | 10-Mar-26 A | 25-Apr-26 A | 0.00 | 0.00 | 0.00 | -10 |
| MLTX-02-005-EN | Pre-Qualification Approval for Galvanized Ducts | 15 | 100% | 100% | 14-Apr-26 | 30-Apr-26 | 14-Mar-26 A | 30-Apr-26 A | 0.00 | 0.00 | 0.00 | 0 |
| **EXHAUST FANS** | | 30 | 0% | 0% | 28-Mar-26 | 30-Apr-26 | 10-Mar-26 A | 08-Apr-26 A | 0.00 | 0.00 | 0.00 | 19 |
| MLTX-02-005-EN | Pre-Qualification Submittal for Exhaust Fans | 15 | 100% | 100% | 28-Mar-26 | 13-Apr-26 | 10-Mar-26 A | 01-Apr-26 A | 0.00 | 0.00 | 0.00 | 10 |
| MLTX-02-005-EN | Pre-Qualification Approval for Exhaust Fans | 15 | 100% | 100% | 14-Apr-26 | 30-Apr-26 | 14-Mar-26 A | 08-Apr-26 A | 0.00 | 0.00 | 0.00 | 19 |
| **LIGHTING FIXTURES** | | 30 | 0% | 0% | 28-Mar-26 | 30-Apr-26 | 10-Mar-26 A | 07-Jun-26 A | 0.00 | 0.00 | 0.00 | -29 |
| MLTX-02-005-EN | Pre-Qualification Submittal for Lighting Fixtures | 15 | 100% | 100% | 28-Mar-26 | 13-Apr-26 | 10-Mar-26 A | 25-May-26 A | 0.00 | 0.00 | 0.00 | -36 |
| MLTX-02-005-EN | Pre-Qualification Approval for Lighting Fixtures | 15 | 100% | 100% | 14-Apr-26 | 30-Apr-26 | 14-Mar-26 A | 07-Jun-26 A | 0.00 | 0.00 | 0.00 | -29 |
| **SWITCHES/SOCKETS** | | 30 | 0% | 0% | 28-Mar-26 | 30-Apr-26 | 10-Mar-26 A | 07-Jun-26 A | 0.00 | 0.00 | 0.00 | -29 |
| MLTX-02-005-EN | Pre-Qualification Submittal for Switches/Sockets | 15 | 100% | 100% | 28-Mar-26 | 13-Apr-26 | 10-Mar-26 A | 25-May-26 A | 0.00 | 0.00 | 0.00 | -36 |
| MLTX-02-005-EN | Pre-Qualification Approval for Switches/Sockets | 15 | 100% | 100% | 14-Apr-26 | 30-Apr-26 | 14-Mar-26 A | 07-Jun-26 A | 0.00 | 0.00 | 0.00 | -29 |
| **EARTHING SYSTEM** | | 30 | 0% | 0% | 28-Mar-26 | 30-Apr-26 | 10-Mar-26 A | 11-May-26 A | 0.00 | 0.00 | 0.00 | -9 |
| MLTX-02-005-EN | Pre-Qualification Submittal for Earthing System | 15 | 100% | 100% | 28-Mar-26 | 13-Apr-26 | 10-Mar-26 A | 09-May-26 A | 0.00 | 0.00 | 0.00 | -22 |
| MLTX-02-005-EN | Pre-Qualification Approval for Earthing System | 15 | 100% | 100% | 14-Apr-26 | 30-Apr-26 | 14-Mar-26 A | 11-May-26 A | 0.00 | 0.00 | 0.00 | -9 |
| **DISTRIBUTION PANNELS** | | 30 | 0% | 0% | 28-Mar-26 | 30-Apr-26 | 10-Mar-26 A | 06-May-26 A | 0.00 | 0.00 | 0.00 | -5 |
| MLTX-02-005-EN | Pre-Qualification Submittal for Distribution Panels | 15 | 100% | 100% | 28-Mar-26 | 13-Apr-26 | 10-Mar-26 A | 30-Apr-26 A | 0.00 | 0.00 | 0.00 | -15 |
| MLTX-02-005-EN | Pre-Qualification Approval for Distribution Panels | 15 | 100% | 100% | 14-Apr-26 | 30-Apr-26 | 14-Mar-26 A | 06-May-26 A | 0.00 | 0.00 | 0.00 | -5 |
| **PLAYGROUND WORKS** | | 45 | 0% | 0% | 07-Mar-26 | 30-Apr-26 | 07-Mar-26 A | 07-Jun-26 A | 0.00 | 0.00 | 0.00 | -29 |

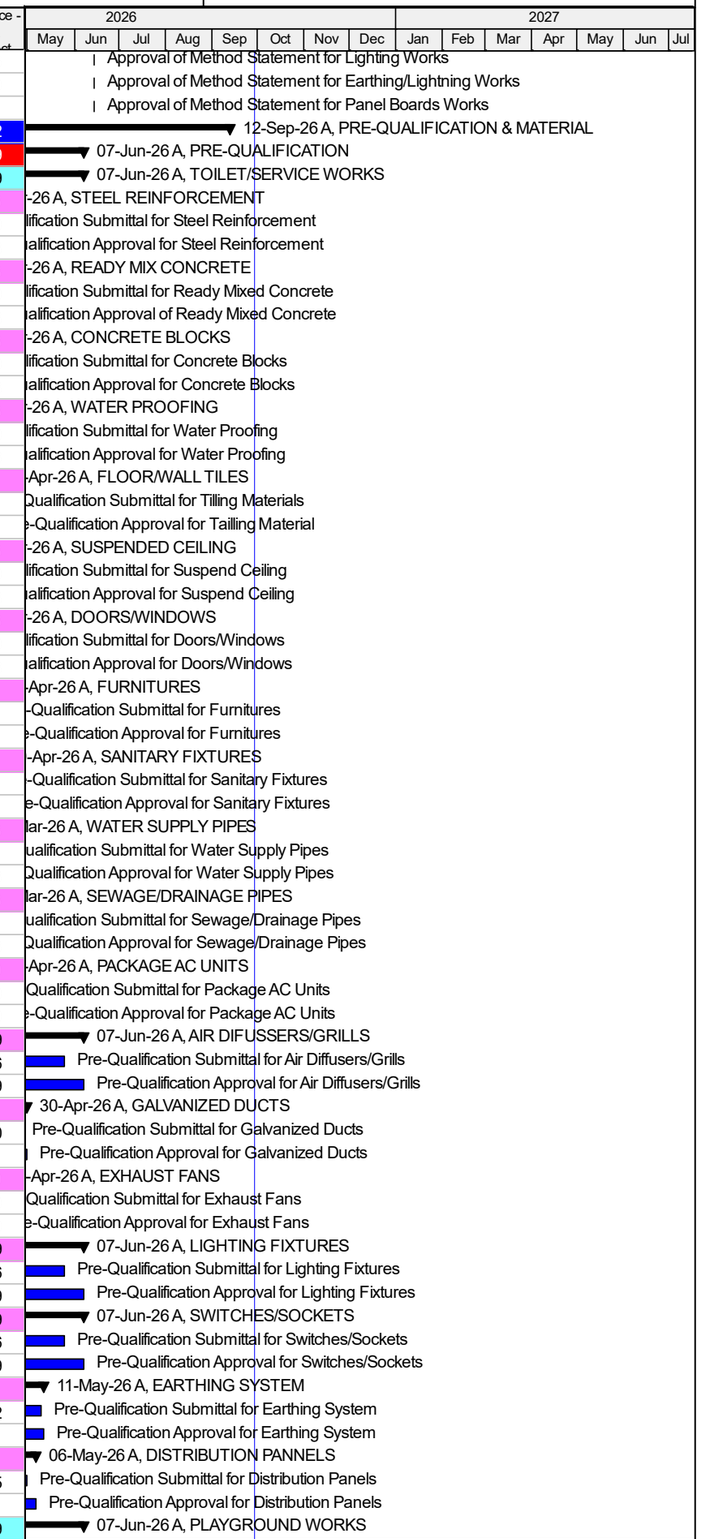





© Oracle Corporation

# MLTX-02-005 - Playground Initiative for Eastern Region (Arar-Hasa osis -Dammam)

**Updateded schedule**
**D.D 28-09-2026**

| Activity ID | Activity Name | Original Duration | Schedule % Complete | Performance % Complete | BL Project Start | BL Project Finish | Start | Finish | Planned Value Cost | Earned Value Cost | Budgeted Total Cost | Variance - BL Project |
|---|---|---|---|---|---|---|---|---|---|---|---|---|
| **PVC MEMBRANE** | | 36 | 0% | 0% | 07-Mar-26 | 20-Apr-26 | 07-Mar-26 A | 24-May-26 A | 0.00 | 0.00 | 0.00 | -29 |
| MLTX-02-005-EI | Pre-Qualification Submittal for PVC Membrane | 15 | 100% | 100% | 07-Mar-26 | 26-Mar-26 | 07-Mar-26 A | 24-May-26 A | 0.00 | 0.00 | 0.00 | -50 |
| MLTX-02-005-EI | Pre-Qualification Approval for PVC Membrane | 21 | 100% | 100% | 28-Mar-26 | 20-Apr-26 | 10-Mar-26 A | 20-May-26 A | 0.00 | 0.00 | 0.00 | -26 |
| **STEEL TENSION CABLES** | | 30 | 0% | 0% | 07-Mar-26 | 13-Apr-26 | 07-Mar-26 A | 24-May-26 A | 0.00 | 0.00 | 0.00 | -35 |
| MLTX-02-005-EI | Pre-Qualification Submittal for Steel Tension Cables | 15 | 100% | 100% | 07-Mar-26 | 26-Mar-26 | 07-Mar-26 A | 20-May-26 A | 0.00 | 0.00 | 0.00 | -47 |
| MLTX-02-005-EI | Pre-Qualification Approval for Steel Tension Cables | 15 | 100% | 100% | 28-Mar-26 | 13-Apr-26 | 10-Mar-26 A | 24-May-26 A | 0.00 | 0.00 | 0.00 | -35 |
| **EMERGENCY DOORS** | | 30 | 0% | 0% | 07-Mar-26 | 13-Apr-26 | 07-Mar-26 A | 24-May-26 A | 0.00 | 0.00 | 0.00 | -35 |
| MLTX-02-005-EI | Pre-Qualification Submittal for Emergency Doors | 15 | 100% | 100% | 07-Mar-26 | 26-Mar-26 | 07-Mar-26 A | 20-May-26 A | 0.00 | 0.00 | 0.00 | -47 |
| MLTX-02-005-EI | Pre-Qualification Approval for Emergency Doors | 15 | 100% | 100% | 28-Mar-26 | 13-Apr-26 | 10-Mar-26 A | 24-May-26 A | 0.00 | 0.00 | 0.00 | -35 |
| **PRESSURE UNITS** | | 30 | 0% | 0% | 07-Mar-26 | 13-Apr-26 | 07-Mar-26 A | 24-May-26 A | 0.00 | 0.00 | 0.00 | -35 |
| MLTX-02-005-EI | Pre-Qualification Submittal for Pressure Units | 15 | 100% | 100% | 07-Mar-26 | 26-Mar-26 | 07-Mar-26 A | 20-May-26 A | 0.00 | 0.00 | 0.00 | -47 |
| MLTX-02-005-EI | Pre-Qualification Approval for Pressure Units | 15 | 100% | 100% | 28-Mar-26 | 13-Apr-26 | 10-Mar-26 A | 24-May-26 A | 0.00 | 0.00 | 0.00 | -35 |
| **AIR LOCK DOORS** | | 30 | 0% | 0% | 07-Mar-26 | 13-Apr-26 | 07-Mar-26 A | 24-May-26 A | 0.00 | 0.00 | 0.00 | -35 |
| MLTX-02-005-EI | Pre-Qualification Submittal for Lock Doors | 15 | 100% | 100% | 07-Mar-26 | 26-Mar-26 | 07-Mar-26 A | 20-May-26 A | 0.00 | 0.00 | 0.00 | -47 |
| MLTX-02-005-EI | Pre-Qualification Approval for Lock Doors | 15 | 100% | 100% | 28-Mar-26 | 13-Apr-26 | 10-Mar-26 A | 24-May-26 A | 0.00 | 0.00 | 0.00 | -35 |
| **ARTIFICIAL TURF** | | 45 | 0% | 0% | 07-Mar-26 | 30-Apr-26 | 07-Mar-26 A | 09-Apr-26 A | 0.00 | 0.00 | 0.00 | 18 |
| MLTX-02-005-EI | Pre-Qualification Submittal for Artificial TURF | 15 | 100% | 100% | 07-Mar-26 | 26-Mar-26 | 07-Mar-26 A | 29-Mar-26 A | 0.00 | 0.00 | 0.00 | -2 |
| MLTX-02-005-EI | Pre-Qualification Approval for Artificial TURF | 30 | 100% | 100% | 28-Mar-26 | 30-Apr-26 | 10-Mar-26 A | 09-Apr-26 A | 0.00 | 0.00 | 0.00 | 18 |
| **RUBBER GRANULES** | | 36 | 0% | 0% | 07-Mar-26 | 20-Apr-26 | 07-Mar-26 A | 10-May-26 A | 0.00 | 0.00 | 0.00 | -17 |
| MLTX-02-005-EI | Pre-Qualification Submittal for Rubber Granules | 15 | 100% | 100% | 07-Mar-26 | 26-Mar-26 | 07-Mar-26 A | 06-May-26 A | 0.00 | 0.00 | 0.00 | -35 |
| MLTX-02-005-EI | Pre-Qualification Approval for Rubber Granules | 21 | 100% | 100% | 28-Mar-26 | 20-Apr-26 | 10-Mar-26 A | 10-May-26 A | 0.00 | 0.00 | 0.00 | -17 |
| **PADEL GLASS** | | 30 | 0% | 0% | 07-Mar-26 | 13-Apr-26 | 07-Mar-26 A | 10-May-26 A | 0.00 | 0.00 | 0.00 | -23 |
| MLTX-02-005-EI | Pre-Qualification Submittal for Padel Glass | 15 | 100% | 100% | 07-Mar-26 | 26-Mar-26 | 07-Mar-26 A | 06-May-26 A | 0.00 | 0.00 | 0.00 | -35 |
| MLTX-02-005-EI | Pre-Qualification Approval for Padel Glass | 15 | 100% | 100% | 28-Mar-26 | 13-Apr-26 | 10-Mar-26 A | 10-May-26 A | 0.00 | 0.00 | 0.00 | -23 |
| **PADEL WIRE MESH/STEEL SETS** | | 30 | 0% | 0% | 07-Mar-26 | 13-Apr-26 | 07-Mar-26 A | 10-May-26 A | 0.00 | 0.00 | 0.00 | -23 |
| MLTX-02-005-EI | Pre-Qualification Submittal for Wire Mesh/Steel Sets | 15 | 100% | 100% | 07-Mar-26 | 26-Mar-26 | 07-Mar-26 A | 06-May-26 A | 0.00 | 0.00 | 0.00 | -35 |
| MLTX-02-005-EI | Pre-Qualification Approval for Wire Mesh/Steel Sets | 15 | 100% | 100% | 28-Mar-26 | 13-Apr-26 | 10-Mar-26 A | 10-May-26 A | 0.00 | 0.00 | 0.00 | -23 |
| **AGGREGATE BASE COURSE** | | 36 | 0% | 0% | 07-Mar-26 | 20-Apr-26 | 07-Mar-26 A | 26-Apr-26 A | 0.00 | 0.00 | 0.00 | -5 |
| MLTX-02-005-EI | Pre-Qualification Submittal for Aggregate Base Course | 15 | 100% | 100% | 07-Mar-26 | 26-Mar-26 | 07-Mar-26 A | 19-Apr-26 A | 0.00 | 0.00 | 0.00 | -20 |
| MLTX-02-005-EI | Pre-Qualification Approval for Aggregate Base Course | 21 | 100% | 100% | 28-Mar-26 | 20-Apr-26 | 10-Mar-26 A | 26-Apr-26 A | 0.00 | 0.00 | 0.00 | -5 |
| **BITUMINOUS BASE & WEARING COURSE** | | 30 | 0% | 0% | 28-Mar-26 | 30-Apr-26 | 10-Mar-26 A | 26-Apr-26 A | 0.00 | 0.00 | 0.00 | 4 |
| MLTX-02-005-EI | Pre-Qualification Submittal for Bituminous Base & Wearing | 15 | 100% | 100% | 28-Mar-26 | 13-Apr-26 | 10-Mar-26 A | 19-Apr-26 A | 0.00 | 0.00 | 0.00 | -5 |
| MLTX-02-005-EI | Pre-Qualification Approval for the Site | 15 | 100% | 100% | 14-Apr-26 | 30-Apr-26 | 14-Mar-26 A | 26-Apr-26 A | 0.00 | 0.00 | 0.00 | 4 |
| **INTERLOCKING PAVING** | | 30 | 0% | 0% | 28-Mar-26 | 30-Apr-26 | 12-Mar-26 A | 24-Mar-26 A | 0.00 | 0.00 | 0.00 | 32 |
| MLTX-02-005-EI | Pre-Qualification Submittal for Interlocking Block Pavers | 15 | 100% | 100% | 28-Mar-26 | 13-Apr-26 | 12-Mar-26 A | 15-Mar-26 A | 0.00 | 0.00 | 0.00 | 22 |
| MLTX-02-005-EI | Pre-Qualification Approval for Interlocking Block Pavers | 15 | 100% | 100% | 14-Apr-26 | 30-Apr-26 | 16-Mar-26 A | 24-Mar-26 A | 0.00 | 0.00 | 0.00 | 32 |
| **MARKING PAINT** | | 30 | 0% | 0% | 28-Mar-26 | 30-Apr-26 | 10-Mar-26 A | 09-May-26 A | 0.00 | 0.00 | 0.00 | -7 |
| MLTX-02-005-EI | Pre-Qualification Submittal for Marking Paint | 15 | 100% | 100% | 28-Mar-26 | 13-Apr-26 | 10-Mar-26 A | 05-May-26 A | 0.00 | 0.00 | 0.00 | -19 |
| MLTX-02-005-EI | Pre-Qualification Approval for Marking Paint | 15 | 100% | 100% | 14-Apr-26 | 30-Apr-26 | 14-Mar-26 A | 09-May-26 A | 0.00 | 0.00 | 0.00 | -7 |
| **PACKAGE AC UNITS** | | 30 | 0% | 0% | 28-Mar-26 | 30-Apr-26 | 10-Mar-26 A | 07-Apr-26 A | 0.00 | 0.00 | 0.00 | 20 |
| MLTX-02-005-EI | Pre-Qualification Submittal for Package AC Units | 15 | 100% | 100% | 28-Mar-26 | 13-Apr-26 | 10-Mar-26 A | 01-Apr-26 A | 0.00 | 0.00 | 0.00 | 10 |
| MLTX-02-005-EI | Pre-Qualification Approval for Package AC Units | 15 | 100% | 100% | 14-Apr-26 | 30-Apr-26 | 14-Mar-26 A | 07-Apr-26 A | 0.00 | 0.00 | 0.00 | 20 |
| **AIR DIFUSSERS/GRILLS** | | 30 | 0% | 0% | 28-Mar-26 | 30-Apr-26 | 10-Mar-26 A | 30-Apr-26 A | 0.00 | 0.00 | 0.00 | 0 |
| MLTX-02-005-EI | Pre-Qualification Submittal for Air Difussers/Grills | 15 | 100% | 100% | 28-Mar-26 | 13-Apr-26 | 10-Mar-26 A | 26-Apr-26 A | 0.00 | 0.00 | 0.00 | -11 |
| MLTX-02-005-EI | Pre-Qualification Approval for Air Difussers/Grills | 15 | 100% | 100% | 14-Apr-26 | 30-Apr-26 | 14-Mar-26 A | 30-Apr-26 A | 0.00 | 0.00 | 0.00 | 0 |
| **GALVANIZED DUCTS** | | 30 | 0% | 0% | 28-Mar-26 | 30-Apr-26 | 10-Mar-26 A | 30-Apr-26 A | 0.00 | 0.00 | 0.00 | 0 |
| MLTX-02-005-EI | Pre-Qualification Submittal for Galvanized Duct | 15 | 100% | 100% | 28-Mar-26 | 13-Apr-26 | 10-Mar-26 A | 26-Apr-26 A | 0.00 | 0.00 | 0.00 | -11 |
| MLTX-02-005-EI | Pre-Qualification Approval for Galvanized Duct | 15 | 100% | 100% | 14-Apr-26 | 30-Apr-26 | 14-Mar-26 A | 30-Apr-26 A | 0.00 | 0.00 | 0.00 | 0 |
| **EXHAUST FANS** | | 30 | 0% | 0% | 28-Mar-26 | 30-Apr-26 | 10-Mar-26 A | 08-Apr-26 A | 0.00 | 0.00 | 0.00 | 19 |
| MLTX-02-005-EI | Pre-Qualification Submittal for Exhaust Fans | 15 | 100% | 100% | 28-Mar-26 | 13-Apr-26 | 10-Mar-26 A | 01-Apr-26 A | 0.00 | 0.00 | 0.00 | 10 |
| MLTX-02-005-EI | Pre-Qualification Approval for Exhaust Fans | 15 | 100% | 100% | 14-Apr-26 | 30-Apr-26 | 14-Mar-26 A | 08-Apr-26 A | 0.00 | 0.00 | 0.00 | 19 |
| **DISTRIBUTION BOARDS** | | 30 | 0% | 0% | 28-Mar-26 | 30-Apr-26 | 10-Mar-26 A | 07-Jun-26 A | 0.00 | 0.00 | 0.00 | -29 |
| MLTX-02-005-EI | Pre-Qualification Submittal for Distribution Boards | 15 | 100% | 100% | 28-Mar-26 | 13-Apr-26 | 10-Mar-26 A | 25-May-26 A | 0.00 | 0.00 | 0.00 | -36 |
| MLTX-02-005-EI | Pre-Qualification Approval for Distribution Boards | 15 | 100% | 100% | 14-Apr-26 | 30-Apr-26 | 14-Mar-26 A | 07-Jun-26 A | 0.00 | 0.00 | 0.00 | -29 |
| **POWER CABLES** | | 30 | 0% | 0% | 28-Mar-26 | 30-Apr-26 | 10-Mar-26 A | 11-May-26 A | 0.00 | 0.00 | 0.00 | -9 |
| MLTX-02-005-EI | Pre-Qualification Submittal for Power Cables | 15 | 100% | 100% | 28-Mar-26 | 13-Apr-26 | 10-Mar-26 A | 09-May-26 A | 0.00 | 0.00 | 0.00 | -22 |
| MLTX-02-005-EI | Pre-Qualification Approval for Power Cables | 15 | 100% | 100% | 14-Apr-26 | 30-Apr-26 | 14-Mar-26 A | 11-May-26 A | 0.00 | 0.00 | 0.00 | -9 |
| **LIGHT FIXTURES** | | 30 | 0% | 0% | 28-Mar-26 | 30-Apr-26 | 10-Mar-26 A | 07-Jun-26 A | 0.00 | 0.00 | 0.00 | -29 |
| MLTX-02-005-EI | Pre-Qualification Submittal for Light Fixtures | 15 | 100% | 100% | 28-Mar-26 | 13-Apr-26 | 10-Mar-26 A | 25-May-26 A | 0.00 | 0.00 | 0.00 | -36 |
| MLTX-02-005-EI | Pre-Qualification Approval for Light Fixtures | 15 | 100% | 100% | 14-Apr-26 | 30-Apr-26 | 14-Mar-26 A | 07-Jun-26 A | 0.00 | 0.00 | 0.00 | -29 |
| **CCTV MATERIALS** | | 30 | 0% | 0% | 28-Mar-26 | 30-Apr-26 | 10-Mar-26 A | 07-Jun-26 A | 0.00 | 0.00 | 0.00 | -29 |
| MLTX-02-005-EI | Pre-Qualification Submittal for CCTV | 15 | 100% | 100% | 28-Mar-26 | 13-Apr-26 | 10-Mar-26 A | 25-May-26 A | 0.00 | 0.00 | 0.00 | -36 |
| MLTX-02-005-EI | Pre-Qualification Approval for CCTV | 15 | 100% | 100% | 14-Apr-26 | 30-Apr-26 | 14-Mar-26 A | 07-Jun-26 A | 0.00 | 0.00 | 0.00 | -29 |
| **POWER OUTLETS/SWITCHES** | | 30 | 0% | 0% | 28-Mar-26 | 30-Apr-26 | 10-Mar-26 A | 07-Jun-26 A | 0.00 | 0.00 | 0.00 | -29 |

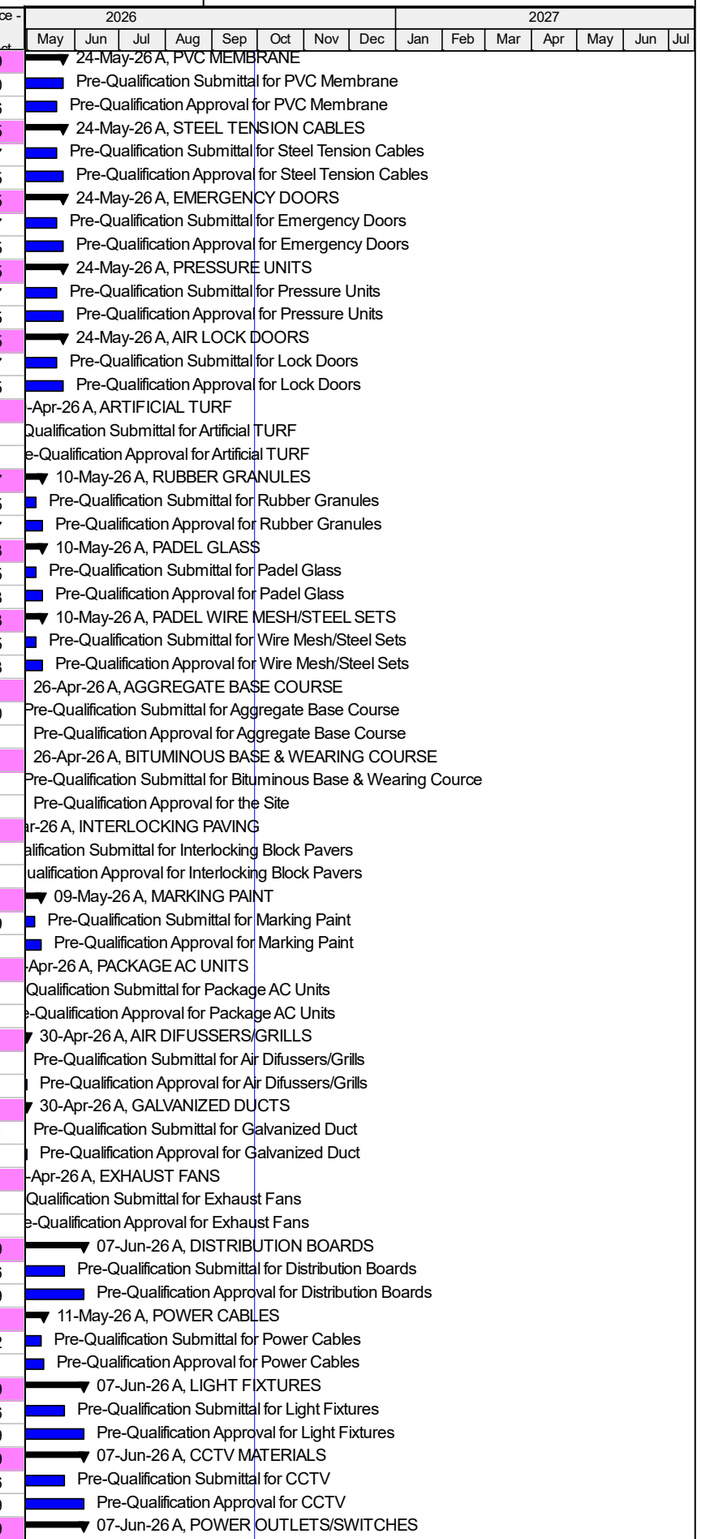


Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary




TASK filter: All Activities

© Oracle Corporation

# MLTX-02-005 - Playground Initiative for Eastern Region (Arar-Hasa osis -Dammam)

**Updateded schedule**
**D.D 28-09-2026**

| Activity ID | Activity Name | Original Duration | Schedule % Complete | Performance % Complete | BL Project Start | BL Project Finish | Start | Finish | Planned Value Cost | Earned Value Cost | Budgeted Total Cost | Variance - BL Project |
|---|---|---|---|---|---|---|---|---|---|---|---|---|
| MLTX-02-005-EN | Pre-Qualification Submittal for Power Outlets/Switches | 15 | 100% | 100% | 28-Mar-26 | 13-Apr-26 | 10-Mar-26 A | 25-May-26 A | 0.00 | 0.00 | 0.00 | -36 |
| MLTX-02-005-EN | Pre-Qualification Approval for Power Outlets/Switches | 15 | 100% | 100% | 14-Apr-26 | 30-Apr-26 | 14-Mar-26 A | 07-Jun-26 A | 0.00 | 0.00 | 0.00 | -29 |
| **LANDSCAPE WORKS** | | 30 | 0% | 0% | 28-Mar-26 | 30-Apr-26 | 10-Mar-26 A | 11-May-26 A | 0.00 | 0.00 | 0.00 | -9 |
| **INTERLOCKING PAVING** | | 30 | 0% | 0% | 28-Mar-26 | 30-Apr-26 | 12-Mar-26 A | 24-Mar-26 A | 0.00 | 0.00 | 0.00 | 32 |
| MLTX-02-005-EN | Pre-Qualification Submittal for Interlocking Block Pavers | 15 | 100% | 100% | 28-Mar-26 | 13-Apr-26 | 12-Mar-26 A | 15-Mar-26 A | 0.00 | 0.00 | 0.00 | 22 |
| MLTX-02-005-EN | Pre-Qualification Approval for Interlocking Block Pavers | 15 | 100% | 100% | 14-Apr-26 | 30-Apr-26 | 16-Mar-26 A | 24-Mar-26 A | 0.00 | 0.00 | 0.00 | 32 |
| **CURBSTONE** | | 30 | 0% | 0% | 28-Mar-26 | 30-Apr-26 | 12-Mar-26 A | 24-Mar-26 A | 0.00 | 0.00 | 0.00 | 32 |
| MLTX-02-005-EN | Pre-Qualification Submittal for Curbstone | 15 | 100% | 100% | 28-Mar-26 | 13-Apr-26 | 12-Mar-26 A | 15-Mar-26 A | 0.00 | 0.00 | 0.00 | 22 |
| MLTX-02-005-EN | Pre-Qualification Approval for Curbstone | 15 | 100% | 100% | 14-Apr-26 | 30-Apr-26 | 16-Mar-26 A | 24-Mar-26 A | 0.00 | 0.00 | 0.00 | 32 |
| **PAVEMENT MARKING** | | 30 | 0% | 0% | 28-Mar-26 | 30-Apr-26 | 10-Mar-26 A | 09-May-26 A | 0.00 | 0.00 | 0.00 | -7 |
| MLTX-02-005-EN | Pre-Qualification Submittal for Pavement Markings | 15 | 100% | 100% | 28-Mar-26 | 13-Apr-26 | 10-Mar-26 A | 05-May-26 A | 0.00 | 0.00 | 0.00 | -19 |
| MLTX-02-005-EN | Pre-Qualification Approval for Pavement Markings | 15 | 100% | 100% | 14-Apr-26 | 30-Apr-26 | 14-Mar-26 A | 09-May-26 A | 0.00 | 0.00 | 0.00 | -7 |
| **TRAFFIC SIGNS** | | 30 | 0% | 0% | 28-Mar-26 | 30-Apr-26 | 10-Mar-26 A | 09-May-26 A | 0.00 | 0.00 | 0.00 | -7 |
| MLTX-02-005-EN | Pre-Qualification Submittal for Traffic Signs | 15 | 100% | 100% | 28-Mar-26 | 13-Apr-26 | 10-Mar-26 A | 05-May-26 A | 0.00 | 0.00 | 0.00 | -19 |
| MLTX-02-005-EN | Pre-Qualification Approval for Traffic Signs | 15 | 100% | 100% | 14-Apr-26 | 30-Apr-26 | 14-Mar-26 A | 09-May-26 A | 0.00 | 0.00 | 0.00 | -7 |
| **IRRIGATION PIPES/SPRINKLERS** | | 30 | 0% | 0% | 28-Mar-26 | 30-Apr-26 | 10-Mar-26 A | 05-May-26 A | 0.00 | 0.00 | 0.00 | -4 |
| MLTX-02-005-EN | Pre-Qualification Submittal for Irrigation Pipes/Sprinkles | 15 | 100% | 100% | 28-Mar-26 | 13-Apr-26 | 10-Mar-26 A | 14-Apr-26 A | 0.00 | 0.00 | 0.00 | -1 |
| MLTX-02-005-EN | Pre-Qualification Approval for Irrigation Pipes/Sprinkles | 15 | 100% | 100% | 14-Apr-26 | 30-Apr-26 | 14-Mar-26 A | 05-May-26 A | 0.00 | 0.00 | 0.00 | -4 |
| **AGRICULTURE SOIL** | | 30 | 0% | 0% | 28-Mar-26 | 30-Apr-26 | 10-Mar-26 A | 05-May-26 A | 0.00 | 0.00 | 0.00 | -4 |
| MLTX-02-005-EN | Pre-Qualification Submittal for Agriculture Soil | 15 | 100% | 100% | 28-Mar-26 | 13-Apr-26 | 10-Mar-26 A | 14-Apr-26 A | 0.00 | 0.00 | 0.00 | -1 |
| MLTX-02-005-EN | Pre-Qualification Approval for Agriculture Soil | 15 | 100% | 100% | 14-Apr-26 | 30-Apr-26 | 14-Mar-26 A | 05-May-26 A | 0.00 | 0.00 | 0.00 | -4 |
| **TRACK SURFACE** | | 30 | 0% | 0% | 28-Mar-26 | 30-Apr-26 | 10-Mar-26 A | 05-May-26 A | 0.00 | 0.00 | 0.00 | -4 |
| MLTX-02-005-EN | Pre-Qualification Submittal for Track Surface | 15 | 100% | 100% | 28-Mar-26 | 13-Apr-26 | 10-Mar-26 A | 19-Apr-26 A | 0.00 | 0.00 | 0.00 | -5 |
| MLTX-02-005-EN | Pre-Qualification Approval for Track Surface | 15 | 100% | 100% | 14-Apr-26 | 30-Apr-26 | 14-Mar-26 A | 05-May-26 A | 0.00 | 0.00 | 0.00 | -4 |
| **GRASS/TREES** | | 30 | 0% | 0% | 28-Mar-26 | 30-Apr-26 | 10-Mar-26 A | 05-May-26 A | 0.00 | 0.00 | 0.00 | -4 |
| MLTX-02-005-EN | Pre-Qualification Submittal for Grass/Trees | 15 | 100% | 100% | 28-Mar-26 | 13-Apr-26 | 10-Mar-26 A | 14-Apr-26 A | 0.00 | 0.00 | 0.00 | -1 |
| MLTX-02-005-EN | Pre-Qualification Approval for Grass/Trees | 15 | 100% | 100% | 14-Apr-26 | 30-Apr-26 | 14-Mar-26 A | 05-May-26 A | 0.00 | 0.00 | 0.00 | -4 |
| **CABLES** | | 30 | 0% | 0% | 28-Mar-26 | 30-Apr-26 | 10-Mar-26 A | 11-May-26 A | 0.00 | 0.00 | 0.00 | -9 |
| MLTX-02-005-EN | Pre-Qualification Submittal for Cables | 15 | 100% | 100% | 28-Mar-26 | 13-Apr-26 | 10-Mar-26 A | 09-May-26 A | 0.00 | 0.00 | 0.00 | -22 |
| MLTX-02-005-EN | Pre-Qualification Approval for Cables | 15 | 100% | 100% | 14-Apr-26 | 30-Apr-26 | 14-Mar-26 A | 11-May-26 A | 0.00 | 0.00 | 0.00 | -9 |
| **LIGHT POLES** | | 30 | 0% | 0% | 28-Mar-26 | 30-Apr-26 | 10-Mar-26 A | 30-Apr-26 A | 0.00 | 0.00 | 0.00 | 0 |
| MLTX-02-005-EN | Pre-Qualification Submittal for Lighting poles | 15 | 100% | 100% | 28-Mar-26 | 13-Apr-26 | 10-Mar-26 A | 26-Apr-26 A | 0.00 | 0.00 | 0.00 | -11 |
| MLTX-02-005-EN | Pre-Qualification Approval for Lighting poles | 15 | 100% | 100% | 14-Apr-26 | 30-Apr-26 | 14-Mar-26 A | 30-Apr-26 A | 0.00 | 0.00 | 0.00 | 0 |
| **MATERIAL SUBMITTAL & APPROVAL** | | 94 | 0% | 0% | 14-Apr-26 | 13-Jul-26 | 18-Mar-26 A | 12-Sep-26 A | 0.00 | 0.00 | 0.00 | -52 |
| **TOILET/SERVICE WORKS** | | 64 | 0% | 0% | 14-Apr-26 | 08-Jun-26 | 18-Mar-26 A | 11-Jul-26 A | 0.00 | 0.00 | 0.00 | -28 |
| **STEEL REINFORCEMENT** | | 30 | 0% | 0% | 14-Apr-26 | 18-May-26 | 18-Mar-26 A | 12-Apr-26 A | 0.00 | 0.00 | 0.00 | 31 |
| MLTX-02-005-EN | Material Submittal for Steel Reinforcement | 15 | 100% | 100% | 14-Apr-26 | 30-Apr-26 | 18-Mar-26 A | 07-Apr-26 A | 0.00 | 0.00 | 0.00 | 20 |
| MLTX-02-005-EN | Material Approval for Steel Reinforcement | 15 | 100% | 100% | 02-May-26 | 18-May-26 | 25-Mar-26 A | 12-Apr-26 A | 0.00 | 0.00 | 0.00 | 31 |
| **READY MIX CONCRETE** | | 30 | 0% | 0% | 14-Apr-26 | 18-May-26 | 18-Mar-26 A | 12-Apr-26 A | 0.00 | 0.00 | 0.00 | 31 |
| MLTX-02-005-EN | Material Submittal for Ready Mixed Concrete | 15 | 100% | 100% | 14-Apr-26 | 30-Apr-26 | 18-Mar-26 A | 07-Apr-26 A | 0.00 | 0.00 | 0.00 | 20 |
| MLTX-02-005-EN | Material Approval of Ready Mixed Concrete | 15 | 100% | 100% | 02-May-26 | 18-May-26 | 25-Mar-26 A | 12-Apr-26 A | 0.00 | 0.00 | 0.00 | 31 |
| **CONCRETE BLOCKS** | | 30 | 0% | 0% | 14-Apr-26 | 18-May-26 | 18-Mar-26 A | 11-May-26 A | 0.00 | 0.00 | 0.00 | 6 |
| MLTX-02-005-EN | Material Submittal for Concrete Blocks | 15 | 100% | 100% | 14-Apr-26 | 30-Apr-26 | 18-Mar-26 A | 06-May-26 A | 0.00 | 0.00 | 0.00 | -5 |
| MLTX-02-005-EN | Material Approval for Concrete Blocks | 15 | 100% | 100% | 02-May-26 | 18-May-26 | 25-Mar-26 A | 11-May-26 A | 0.00 | 0.00 | 0.00 | 6 |
| **FLOOR/WALL TILES** | | 30 | 0% | 0% | 14-Apr-26 | 18-May-26 | 18-Mar-26 A | 17-May-26 A | 0.00 | 0.00 | 0.00 | 1 |
| MLTX-02-005-EN | Material Submittal for Tilling Materials | 15 | 100% | 100% | 14-Apr-26 | 30-Apr-26 | 18-Mar-26 A | 13-May-26 A | 0.00 | 0.00 | 0.00 | -11 |
| MLTX-02-005-EN | Material Approval for Tilling Material | 15 | 100% | 100% | 02-May-26 | 18-May-26 | 25-Mar-26 A | 17-May-26 A | 0.00 | 0.00 | 0.00 | 1 |
| **SUSPENDED CEILING** | | 30 | 0% | 0% | 14-Apr-26 | 18-May-26 | 18-Mar-26 A | 19-Apr-26 A | 0.00 | 0.00 | 0.00 | 25 |
| MLTX-02-005-EN | Material Submittal for Suspend Ceiling | 15 | 100% | 100% | 14-Apr-26 | 30-Apr-26 | 18-Mar-26 A | 15-Apr-26 A | 0.00 | 0.00 | 0.00 | 13 |
| MLTX-02-005-EN | Material Approval for Suspend Ceiling | 15 | 100% | 100% | 02-May-26 | 18-May-26 | 25-Mar-26 A | 19-Apr-26 A | 0.00 | 0.00 | 0.00 | 25 |
| **DOORS/WINDOWS** | | 30 | 0% | 0% | 14-Apr-26 | 18-May-26 | 18-Mar-26 A | 06-May-26 A | 0.00 | 0.00 | 0.00 | 10 |
| MLTX-02-005-EN | Material Submittal for Doors/Windows | 15 | 100% | 100% | 14-Apr-26 | 30-Apr-26 | 18-Mar-26 A | 06-May-26 A | 0.00 | 0.00 | 0.00 | -5 |
| MLTX-02-005-EN | Material Approval for Doors/Windows | 15 | 100% | 100% | 02-May-26 | 18-May-26 | 25-Mar-26 A | 12-Apr-26 A | 0.00 | 0.00 | 0.00 | 31 |
| **FURNITURES** | | 30 | 0% | 0% | 14-Apr-26 | 18-May-26 | 18-Mar-26 A | 07-Apr-26 A | 0.00 | 0.00 | 0.00 | 35 |
| MLTX-02-005-EN | Material Submittal for Furnitures | 15 | 100% | 100% | 14-Apr-26 | 30-Apr-26 | 18-Mar-26 A | 02-Apr-26 A | 0.00 | 0.00 | 0.00 | 24 |
| MLTX-02-005-EN | Material Approval for Furnitures | 15 | 100% | 100% | 02-May-26 | 18-May-26 | 25-Mar-26 A | 07-Apr-26 A | 0.00 | 0.00 | 0.00 | 35 |
| **SANITARY FIXTURES** | | 30 | 0% | 0% | 14-Apr-26 | 18-May-26 | 18-Mar-26 A | 16-Apr-26 A | 0.00 | 0.00 | 0.00 | 27 |
| MLTX-02-005-EN | Material Submittal for Sanitary Fixtures | 15 | 100% | 100% | 14-Apr-26 | 30-Apr-26 | 18-Mar-26 A | 13-Apr-26 A | 0.00 | 0.00 | 0.00 | 15 |
| MLTX-02-005-EN | Material Approval for Sanitary Fixtures | 15 | 100% | 100% | 02-May-26 | 18-May-26 | 25-Mar-26 A | 16-Apr-26 A | 0.00 | 0.00 | 0.00 | 27 |
| **WATER SUPPLY PIPES** | | 30 | 0% | 0% | 14-Apr-26 | 18-May-26 | 18-Mar-26 A | 16-Apr-26 A | 0.00 | 0.00 | 0.00 | 27 |
| MLTX-02-005-EN | Material Submittal for Water Supply Pipes | 15 | 100% | 100% | 14-Apr-26 | 30-Apr-26 | 18-Mar-26 A | 04-Apr-26 A | 0.00 | 0.00 | 0.00 | 23 |
| MLTX-02-005-EN | Material Approval for Water Supply Pipes | 15 | 100% | 100% | 02-May-26 | 18-May-26 | 25-Mar-26 A | 16-Apr-26 A | 0.00 | 0.00 | 0.00 | 27 |
| **SEWAGE/DRAINAGE PIPES** | | 30 | 0% | 0% | 14-Apr-26 | 18-May-26 | 18-Mar-26 A | 16-Apr-26 A | 0.00 | 0.00 | 0.00 | 27 |
| MLTX-02-005-EN | Material Submittal for Sewage/Drainage Pipes | 15 | 100% | 100% | 14-Apr-26 | 30-Apr-26 | 18-Mar-26 A | 04-Apr-26 A | 0.00 | 0.00 | 0.00 | 23 |

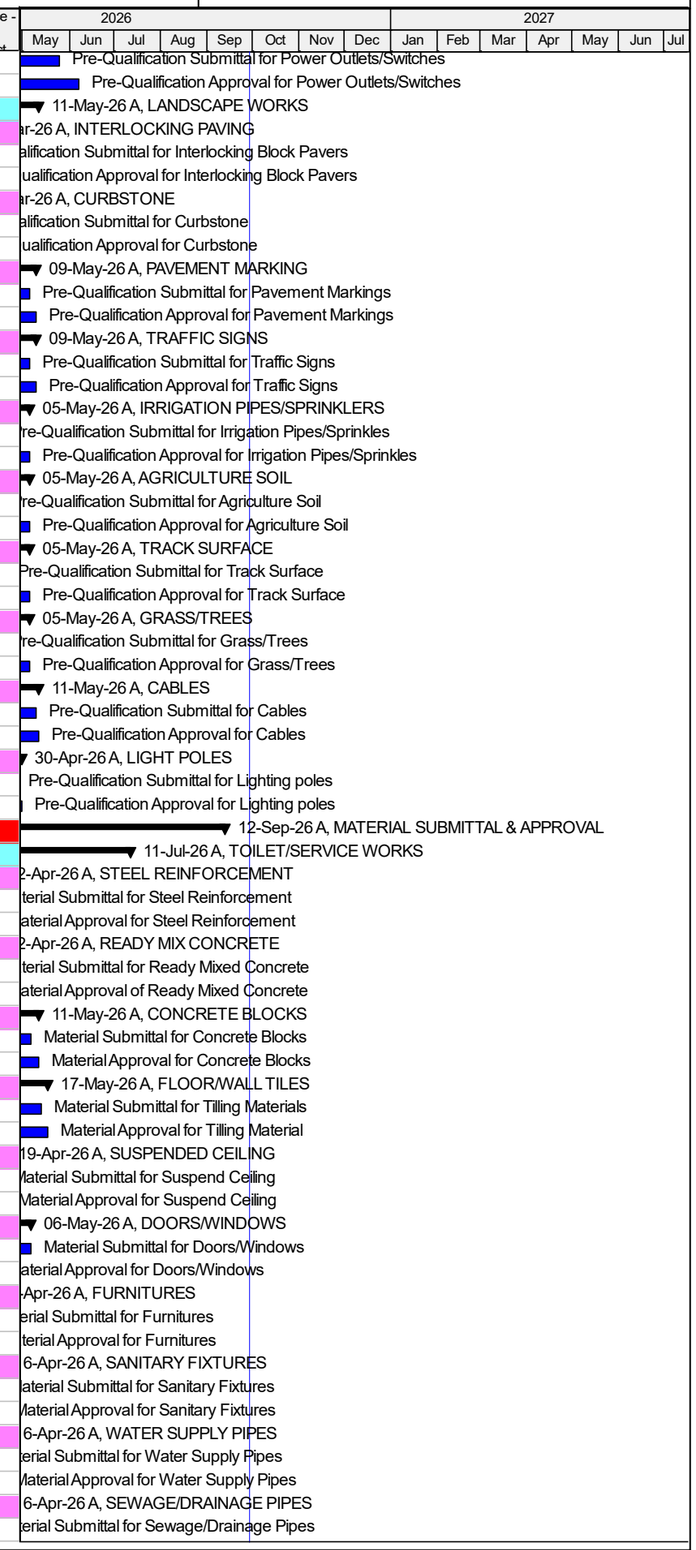




© Oracle Corporation

# MLTX-02-005 - Playground Initiative for Eastern Region (Arar-Hasa osis -Dammam)

**Updateded schedule**
**D.D 28-09-2026**

| Activity ID | Activity Name | Original Duration | Schedule % Complete | Performance % Complete | BL Project Start | BL Project Finish | Start | Finish | Planned Value Cost | Earned Value Cost | Budgeted Total Cost | Variance - BL Project |
|---|---|---|---|---|---|---|---|---|---|---|---|---|
| MLTX-02-005-EM | Material Approval for Sewage/Drainage Pipes | 15 | 100% | 100% | 02-May-26 | 18-May-26 | 25-Mar-26 A | 16-Apr-26 A | 0.00 | 0.00 | 0.00 | 27 |
| **PACKAGE AC UNITS** | | 30 | 0% | 0% | 02-May-26 | 08-Jun-26 | 21-Jun-26 A | 02-Jul-26 A | 0.00 | 0.00 | 0.00 | -21 |
| MLTX-02-005-EM | Material Submittal for Package AC Units | 15 | 100% | 100% | 02-May-26 | 18-May-26 | 21-Jun-26 A | 21-Jun-26 A | 0.00 | 0.00 | 0.00 | -26 |
| MLTX-02-005-EM | Material Approval for Package AC Units | 15 | 100% | 100% | 19-May-26 | 08-Jun-26 | 02-Jul-26 A | 02-Jul-26 A | 0.00 | 0.00 | 0.00 | -21 |
| **AIR DIFUSSERS/GRILLS** | | 30 | 0% | 0% | 02-May-26 | 08-Jun-26 | 11-Jun-26 A | 11-Jun-26 A | 0.00 | 0.00 | 0.00 | -3 |
| MLTX-02-005-EM | Material Submittal for Air Diffusers/Grills | 15 | 100% | 100% | 02-May-26 | 18-May-26 | 11-Jun-26 A | 11-Jun-26 A | 0.00 | 0.00 | 0.00 | -18 |
| MLTX-02-005-EM | Material Approval for Air Diffusers/Grills | 15 | 100% | 100% | 19-May-26 | 08-Jun-26 | 11-Jun-26 A | 11-Jun-26 A | 0.00 | 0.00 | 0.00 | -3 |
| **GALVANIZED DUCTS** | | 30 | 0% | 0% | 02-May-26 | 08-Jun-26 | 19-Mar-26 A | 10-May-26 A | 0.00 | 0.00 | 0.00 | 22 |
| MLTX-02-005-EM | Material Submittal for Galvanized Ducts | 15 | 100% | 100% | 02-May-26 | 18-May-26 | 19-Mar-26 A | 06-May-26 A | 0.00 | 0.00 | 0.00 | 10 |
| MLTX-02-005-EM | Material Approval for Galvanized Ducts | 15 | 100% | 100% | 19-May-26 | 08-Jun-26 | 26-Mar-26 A | 10-May-26 A | 0.00 | 0.00 | 0.00 | 22 |
| **EXHAUST FANS** | | 30 | 0% | 0% | 02-May-26 | 08-Jun-26 | 11-Jun-26 A | 11-Jun-26 A | 0.00 | 0.00 | 0.00 | -3 |
| MLTX-02-005-EM | Material Submittal for Exhaust Fans | 15 | 100% | 100% | 02-May-26 | 18-May-26 | 11-Jun-26 A | 11-Jun-26 A | 0.00 | 0.00 | 0.00 | -18 |
| MLTX-02-005-EM | Material Approval for Exhaust Fans | 15 | 100% | 100% | 19-May-26 | 08-Jun-26 | 11-Jun-26 A | 11-Jun-26 A | 0.00 | 0.00 | 0.00 | -3 |
| **LIGHTING FIXTURES** | | 30 | 0% | 0% | 02-May-26 | 08-Jun-26 | 11-Jul-26 A | 11-Jul-26 A | 0.00 | 0.00 | 0.00 | -28 |
| MLTX-02-005-EM | Material Submittal for Lighting Fixtures | 15 | 100% | 100% | 02-May-26 | 18-May-26 | 11-Jul-26 A | 11-Jul-26 A | 0.00 | 0.00 | 0.00 | -43 |
| MLTX-02-005-EM | Material Approval for Lighting Fixtures | 15 | 100% | 100% | 19-May-26 | 08-Jun-26 | 11-Jul-26 A | 11-Jul-26 A | 0.00 | 0.00 | 0.00 | -28 |
| **SWITCHES/SOCKETS** | | 30 | 0% | 0% | 02-May-26 | 08-Jun-26 | 25-Jun-26 A | 27-Jun-26 A | 0.00 | 0.00 | 0.00 | -16 |
| MLTX-02-005-EM | Material Submittal for Switches/Sockets | 15 | 100% | 100% | 02-May-26 | 18-May-26 | 25-Jun-26 A | 25-Jun-26 A | 0.00 | 0.00 | 0.00 | -30 |
| MLTX-02-005-EM | Material Approval for Switches/Sockets | 15 | 100% | 100% | 19-May-26 | 08-Jun-26 | 27-Jun-26 A | 27-Jun-26 A | 0.00 | 0.00 | 0.00 | -16 |
| **EARTHING SYSTEM** | | 30 | 0% | 0% | 02-May-26 | 08-Jun-26 | 19-Mar-26 A | 19-May-26 A | 0.00 | 0.00 | 0.00 | 14 |
| MLTX-02-005-EM | Material Submittal for Earthing System | 15 | 100% | 100% | 02-May-26 | 18-May-26 | 19-Mar-26 A | 14-May-26 A | 0.00 | 0.00 | 0.00 | 3 |
| MLTX-02-005-EM | Material Approval for Earthing System | 15 | 100% | 100% | 19-May-26 | 08-Jun-26 | 26-Mar-26 A | 19-May-26 A | 0.00 | 0.00 | 0.00 | 14 |
| **DISTRIBUTION PANNELS** | | 43 | 0% | 0% | 02-May-26 | 08-Jun-26 | 19-Mar-26 A | 18-Jun-26 A | 0.00 | 0.00 | 0.00 | -9 |
| MLTX-02-005-EM | Material Submittal for Distribution Panels | 15 | 100% | 100% | 02-May-26 | 18-May-26 | 19-Mar-26 A | 11-May-26 A | 0.00 | 0.00 | 0.00 | 6 |
| MLTX-02-005-EM | Material Approval for Distribution Panels | 15 | 100% | 100% | 19-May-26 | 08-Jun-26 | 18-Jun-26 A | 18-Jun-26 A | 0.00 | 0.00 | 0.00 | -9 |
| **PLAYGROUND WORKS** | | 94 | 0% | 0% | 14-Apr-26 | 13-Jul-26 | 18-Mar-26 A | 12-Sep-26 A | 0.00 | 0.00 | 0.00 | -52 |
| **PVC MEMBRANE** | | 42 | 0% | 0% | 21-Apr-26 | 11-Jun-26 | 26-Aug-26 A | 26-Aug-26 A | 0.00 | 0.00 | 0.00 | -65 |
| MLTX-02-005-EM | Material Submittal for PVC Membrane | 21 | 100% | 100% | 21-Apr-26 | 14-May-26 | 26-Aug-26 A | 26-Aug-26 A | 0.00 | 0.00 | 0.00 | -86 |
| MLTX-02-005-EM | Material Approval for PVC Membrane | 21 | 100% | 100% | 16-May-26 | 11-Jun-26 | 26-Aug-26 A | 26-Aug-26 A | 0.00 | 0.00 | 0.00 | -65 |
| **STEEL TENSION CABLES** | | 30 | 0% | 0% | 14-Apr-26 | 18-May-26 | 26-Aug-26 A | 26-Aug-26 A | 0.00 | 0.00 | 0.00 | -83 |
| MLTX-02-005-EM | Material Submittal for Steel Tension Cables | 15 | 100% | 100% | 14-Apr-26 | 30-Apr-26 | 26-Aug-26 A | 26-Aug-26 A | 0.00 | 0.00 | 0.00 | -98 |
| MLTX-02-005-EM | Material Approval for Steel Tension Cables | 15 | 100% | 100% | 02-May-26 | 18-May-26 | 26-Aug-26 A | 26-Aug-26 A | 0.00 | 0.00 | 0.00 | -83 |
| **EMERGENCY DOORS** | | 28 | 0% | 0% | 14-Apr-26 | 18-May-26 | 26-Aug-26 A | 12-Sep-26 A | 0.00 | 0.00 | 0.00 | -97 |
| MLTX-02-005-EM | Material Submittal for Emergency Doors | 15 | 100% | 100% | 14-Apr-26 | 30-Apr-26 | 26-Aug-26 A | 26-Aug-26 A | 0.00 | 0.00 | 0.00 | -98 |
| MLTX-02-005-EM | Material Approval for Emergency Doors | 15 | 100% | 100% | 02-May-26 | 18-May-26 | 12-Sep-26 A | 12-Sep-26 A | 0.00 | 0.00 | 0.00 | -97 |
| **PRESSURE UNITS** | | 30 | 0% | 0% | 14-Apr-26 | 18-May-26 | 12-Sep-26 A | 12-Sep-26 A | 0.00 | 0.00 | 0.00 | -97 |
| MLTX-02-005-EM | Material Submittal for Pressure Units | 15 | 100% | 100% | 14-Apr-26 | 30-Apr-26 | 12-Sep-26 A | 12-Sep-26 A | 0.00 | 0.00 | 0.00 | -112 |
| MLTX-02-005-EM | Material Approval for Pressure Units | 15 | 100% | 100% | 02-May-26 | 18-May-26 | 12-Sep-26 A | 12-Sep-26 A | 0.00 | 0.00 | 0.00 | -96 |
| **AIR LOCK DOORS** | | 28 | 0% | 0% | 14-Apr-26 | 18-May-26 | 26-Aug-26 A | 12-Sep-26 A | 0.00 | 0.00 | 0.00 | -97 |
| MLTX-02-005-EM | Material Submittal for Lock Doors | 15 | 100% | 100% | 14-Apr-26 | 30-Apr-26 | 26-Aug-26 A | 26-Aug-26 A | 0.00 | 0.00 | 0.00 | -98 |
| MLTX-02-005-EM | Material Approval for Lock Doors | 15 | 100% | 100% | 02-May-26 | 18-May-26 | 12-Sep-26 A | 12-Sep-26 A | 0.00 | 0.00 | 0.00 | -97 |
| **ARTIFICIAL TURF** | | 60 | 0% | 0% | 02-May-26 | 13-Jul-26 | 18-Mar-26 A | 19-May-26 A | 0.00 | 0.00 | 0.00 | 44 |
| MLTX-02-005-EM | Material Submittal for Artificial TURF | 30 | 100% | 100% | 02-May-26 | 08-Jun-26 | 18-Mar-26 A | 14-May-26 A | 0.00 | 0.00 | 0.00 | 18 |
| MLTX-02-005-EM | Material Approval for Artificial TURF | 30 | 100% | 100% | 09-Jun-26 | 13-Jul-26 | 25-Mar-26 A | 19-May-26 A | 0.00 | 0.00 | 0.00 | 44 |
| **RUBBER GRANULES** | | 42 | 0% | 0% | 21-Apr-26 | 11-Jun-26 | 18-Mar-26 A | 19-May-26 A | 0.00 | 0.00 | 0.00 | 17 |
| MLTX-02-005-EM | Material Submittal for Rubber Granules | 21 | 100% | 100% | 21-Apr-26 | 14-May-26 | 18-Mar-26 A | 14-May-26 A | 0.00 | 0.00 | 0.00 | 0 |
| MLTX-02-005-EM | Material Approval for Rubber Granules | 21 | 100% | 100% | 16-May-26 | 11-Jun-26 | 25-Mar-26 A | 19-May-26 A | 0.00 | 0.00 | 0.00 | 17 |
| **PADEL GLASS** | | 30 | 0% | 0% | 14-Apr-26 | 18-May-26 | 18-Mar-26 A | 19-May-26 A | 0.00 | 0.00 | 0.00 | -1 |
| MLTX-02-005-EM | Material Submittal for Padel Glass | 15 | 100% | 100% | 14-Apr-26 | 30-Apr-26 | 18-Mar-26 A | 14-May-26 A | 0.00 | 0.00 | 0.00 | -12 |
| MLTX-02-005-EM | Material Approval for Padel Glass | 15 | 100% | 100% | 02-May-26 | 18-May-26 | 25-Mar-26 A | 19-May-26 A | 0.00 | 0.00 | 0.00 | -1 |
| **PADEL WIRE MESH/STEEL SETS** | | 30 | 0% | 0% | 14-Apr-26 | 18-May-26 | 18-Mar-26 A | 19-May-26 A | 0.00 | 0.00 | 0.00 | -1 |
| MLTX-02-005-EM | Material Submittal for Wire Mesh/Steel Sets | 15 | 100% | 100% | 14-Apr-26 | 30-Apr-26 | 18-Mar-26 A | 14-May-26 A | 0.00 | 0.00 | 0.00 | -12 |
| MLTX-02-005-EM | Material Approval for Wire Mesh/Steel Sets | 15 | 100% | 100% | 02-May-26 | 18-May-26 | 25-Mar-26 A | 19-May-26 A | 0.00 | 0.00 | 0.00 | -1 |
| **AGGREGATE BASE COURSE** | | 42 | 0% | 0% | 21-Apr-26 | 11-Jun-26 | 18-Mar-26 A | 03-May-26 A | 0.00 | 0.00 | 0.00 | 31 |
| MLTX-02-005-EM | Material Submittal for Aggregate Base Course | 21 | 100% | 100% | 21-Apr-26 | 14-May-26 | 18-Mar-26 A | 30-Apr-26 A | 0.00 | 0.00 | 0.00 | 12 |
| MLTX-02-005-EM | Material Approval for Aggregate Base Course | 21 | 100% | 100% | 16-May-26 | 11-Jun-26 | 25-Mar-26 A | 03-May-26 A | 0.00 | 0.00 | 0.00 | 31 |
| **BITUMINOUS BASE & WEARING COURSE** | | 30 | 0% | 0% | 02-May-26 | 08-Jun-26 | 19-Mar-26 A | 04-May-26 A | 0.00 | 0.00 | 0.00 | 27 |
| MLTX-02-005-EM | Material Submittal for Bituminous Base & Wearing Cource | 15 | 100% | 100% | 02-May-26 | 18-May-26 | 19-Mar-26 A | 30-Apr-26 A | 0.00 | 0.00 | 0.00 | 15 |
| MLTX-02-005-EM | Material Approval for the Site | 15 | 100% | 100% | 19-May-26 | 08-Jun-26 | 26-Mar-26 A | 04-May-26 A | 0.00 | 0.00 | 0.00 | 27 |
| **INTERLOCKING PAVING** | | 30 | 0% | 0% | 02-May-26 | 08-Jun-26 | 19-Mar-26 A | 10-May-26 A | 0.00 | 0.00 | 0.00 | 22 |
| MLTX-02-005-EM | Material Submittal for Interlocking Block Pavers | 15 | 100% | 100% | 02-May-26 | 18-May-26 | 19-Mar-26 A | 05-May-26 A | 0.00 | 0.00 | 0.00 | 11 |
| MLTX-02-005-EM | Material Approval for Interlocking Block Pavers | 15 | 100% | 100% | 19-May-26 | 08-Jun-26 | 26-Mar-26 A | 10-May-26 A | 0.00 | 0.00 | 0.00 | 22 |
| **MARKING PAINT** | | 30 | 0% | 0% | 02-May-26 | 08-Jun-26 | 19-Mar-26 A | 18-May-26 A | 0.00 | 0.00 | 0.00 | 15 |
| MLTX-02-005-EM | Material Submittal for Marking Paint | 15 | 100% | 100% | 02-May-26 | 18-May-26 | 19-Mar-26 A | 13-May-26 A | 0.00 | 0.00 | 0.00 | 4 |

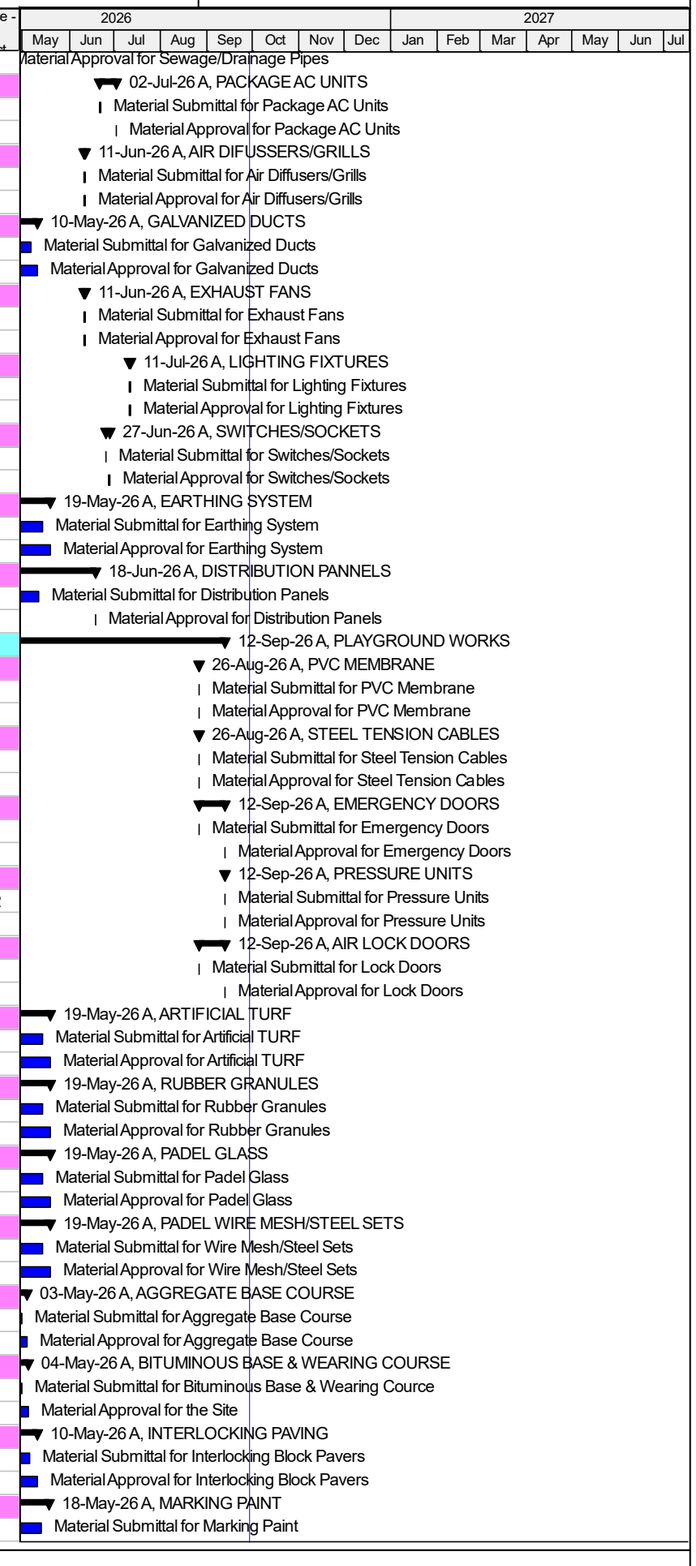





© Oracle Corporation

# MLTX-02-005 - Playground Initiative for Eastern Region (Arar-Hasa osis -Dammam)

**Updateded schedule**
**D.D 28-09-2026**

| Activity ID | Activity Name | Original Duration | Schedule % Complete | Performance % Complete | BL Project Start | BL Project Finish | Start | Finish | Planned Value Cost | Earned Value Cost | Budgeted Total Cost | Variance - BL Project |
|---|---|---|---|---|---|---|---|---|---|---|---|---|
| MLTX-02-005-EM | Material Approval for Marking Paint | 15 | 100% | 100% | 19-May-26 | 08-Jun-26 | 26-Mar-26 A | 18-May-26 A | 0.00 | 0.00 | 0.00 | 15 |
| **PACKAGE AC UNITS** | | 30 | 0% | 0% | 02-May-26 | 08-Jun-26 | 11-Jul-26 A | 11-Jul-26 A | 0.00 | 0.00 | 0.00 | -28 |
| MLTX-02-005-EM | Material Submittal for Package AC Units | 15 | 100% | 100% | 02-May-26 | 18-May-26 | 11-Jul-26 A | 11-Jul-26 A | 0.00 | 0.00 | 0.00 | -43 |
| MLTX-02-005-EM | Material Approval for Package AC Units | 15 | 100% | 100% | 19-May-26 | 08-Jun-26 | 11-Jul-26 A | 11-Jul-26 A | 0.00 | 0.00 | 0.00 | -28 |
| **AIR DIFUSSERS/GRILLS** | | 30 | 0% | 0% | 02-May-26 | 08-Jun-26 | 12-Sep-26 A | 12-Sep-26 A | 0.00 | 0.00 | 0.00 | -82 |
| MLTX-02-005-EM | Material Submittal for Air Difussers/Grills | 15 | 100% | 100% | 02-May-26 | 18-May-26 | 12-Sep-26 A | 12-Sep-26 A | 0.00 | 0.00 | 0.00 | -97 |
| MLTX-02-005-EM | Material Approval for Air Difussers/Grills | 15 | 100% | 100% | 19-May-26 | 08-Jun-26 | 12-Sep-26 A | 12-Sep-26 A | 0.00 | 0.00 | 0.00 | -82 |
| **GALVANIZED DUCTS** | | 30 | 0% | 0% | 02-May-26 | 08-Jun-26 | 19-Mar-26 A | 10-May-26 A | 0.00 | 0.00 | 0.00 | 22 |
| MLTX-02-005-EM | Material Submittal for Galvanized Duct | 15 | 100% | 100% | 02-May-26 | 18-May-26 | 19-Mar-26 A | 06-May-26 A | 0.00 | 0.00 | 0.00 | 10 |
| MLTX-02-005-EM | Material Approval for Galvanized Duct | 15 | 100% | 100% | 19-May-26 | 08-Jun-26 | 26-Mar-26 A | 10-May-26 A | 0.00 | 0.00 | 0.00 | 22 |
| **EXHAUST FANS** | | 30 | 0% | 0% | 02-May-26 | 08-Jun-26 | 11-Jun-26 A | 11-Jun-26 A | 0.00 | 0.00 | 0.00 | -3 |
| MLTX-02-005-EM | Material Submittal for Exhaust Fans | 15 | 100% | 100% | 02-May-26 | 18-May-26 | 11-Jun-26 A | 11-Jun-26 A | 0.00 | 0.00 | 0.00 | -18 |
| MLTX-02-005-EM | Material Approval for Exhaust Fans | 15 | 100% | 100% | 19-May-26 | 08-Jun-26 | 11-Jun-26 A | 11-Jun-26 A | 0.00 | 0.00 | 0.00 | -3 |
| **DISTRIBUTION BOARDS** | | 30 | 0% | 0% | 02-May-26 | 08-Jun-26 | 15-Jun-26 A | 18-Jun-26 A | 0.00 | 0.00 | 0.00 | -9 |
| MLTX-02-005-EM | Material Submittal for Distribution Boards | 15 | 100% | 100% | 02-May-26 | 18-May-26 | 15-Jun-26 A | 15-Jun-26 A | 0.00 | 0.00 | 0.00 | -21 |
| MLTX-02-005-EM | Material Approval for Distribution Boards | 15 | 100% | 100% | 19-May-26 | 08-Jun-26 | 18-Jun-26 A | 18-Jun-26 A | 0.00 | 0.00 | 0.00 | -9 |
| **POWER CABLES** | | 30 | 0% | 0% | 02-May-26 | 08-Jun-26 | 19-Mar-26 A | 19-May-26 A | 0.00 | 0.00 | 0.00 | 14 |
| MLTX-02-005-EM | Material Submittal for Power Cables | 15 | 100% | 100% | 02-May-26 | 18-May-26 | 19-Mar-26 A | 14-May-26 A | 0.00 | 0.00 | 0.00 | 3 |
| MLTX-02-005-EM | Material Approval for Power Cables | 15 | 100% | 100% | 19-May-26 | 08-Jun-26 | 26-Mar-26 A | 19-May-26 A | 0.00 | 0.00 | 0.00 | 14 |
| **LIGHT FIXTURES** | | 30 | 0% | 0% | 02-May-26 | 08-Jun-26 | 11-Jul-26 A | 11-Jul-26 A | 0.00 | 0.00 | 0.00 | -28 |
| MLTX-02-005-EM | Material Submittal for Light Fixtures | 15 | 100% | 100% | 02-May-26 | 18-May-26 | 11-Jul-26 A | 11-Jul-26 A | 0.00 | 0.00 | 0.00 | -43 |
| MLTX-02-005-EM | Material Approval for Light Fixtures | 15 | 100% | 100% | 19-May-26 | 08-Jun-26 | 11-Jul-26 A | 11-Jul-26 A | 0.00 | 0.00 | 0.00 | -28 |
| **CCTV MATERIALS** | | 28 | 0% | 0% | 02-May-26 | 08-Jun-26 | 26-Aug-26 A | 12-Sep-26 A | 0.00 | 0.00 | 0.00 | -82 |
| MLTX-02-005-EM | Material Submittal for CCTV | 15 | 100% | 100% | 02-May-26 | 18-May-26 | 26-Aug-26 A | 26-Aug-26 A | 0.00 | 0.00 | 0.00 | -83 |
| MLTX-02-005-EM | Material Approval for CCTV | 15 | 100% | 100% | 19-May-26 | 08-Jun-26 | 12-Sep-26 A | 12-Sep-26 A | 0.00 | 0.00 | 0.00 | -82 |
| **POWER OUTLETS/SWITCHES** | | 30 | 0% | 0% | 02-May-26 | 08-Jun-26 | 25-Jun-26 A | 27-Jun-26 A | 0.00 | 0.00 | 0.00 | -16 |
| MLTX-02-005-EM | Material Submittal for Power Outlets/Switches | 15 | 100% | 100% | 02-May-26 | 18-May-26 | 25-Jun-26 A | 25-Jun-26 A | 0.00 | 0.00 | 0.00 | -30 |
| MLTX-02-005-EM | Material Approval for Power Outlets/Switches | 15 | 100% | 100% | 19-May-26 | 08-Jun-26 | 27-Jun-26 A | 27-Jun-26 A | 0.00 | 0.00 | 0.00 | -16 |
| **LANDSCAPE WORKS** | | 64 | 0% | 0% | 02-May-26 | 08-Jun-26 | 19-Mar-26 A | 11-Jul-26 A | 0.00 | 0.00 | 0.00 | -28 |
| **INTERLOCKING PAVING** | | 30 | 0% | 0% | 02-May-26 | 08-Jun-26 | 19-Mar-26 A | 10-May-26 A | 0.00 | 0.00 | 0.00 | 22 |
| MLTX-02-005-EM | Material Submittal for Interlocking Block Pavers | 15 | 100% | 100% | 02-May-26 | 18-May-26 | 19-Mar-26 A | 05-May-26 A | 0.00 | 0.00 | 0.00 | 11 |
| MLTX-02-005-EM | Material Approval for Interlocking Block Pavers | 15 | 100% | 100% | 19-May-26 | 08-Jun-26 | 26-Mar-26 A | 10-May-26 A | 0.00 | 0.00 | 0.00 | 22 |
| **CURBSTONE** | | 30 | 0% | 0% | 02-May-26 | 08-Jun-26 | 19-Mar-26 A | 11-May-26 A | 0.00 | 0.00 | 0.00 | 21 |
| MLTX-02-005-EM | Material Submittal for Curbstone | 15 | 100% | 100% | 02-May-26 | 18-May-26 | 19-Mar-26 A | 05-May-26 A | 0.00 | 0.00 | 0.00 | 11 |
| MLTX-02-005-EM | Material Approval for Curbstone | 15 | 100% | 100% | 19-May-26 | 08-Jun-26 | 26-Mar-26 A | 11-May-26 A | 0.00 | 0.00 | 0.00 | 21 |
| **PAVEMENT MARKING** | | 30 | 0% | 0% | 02-May-26 | 08-Jun-26 | 19-Mar-26 A | 18-May-26 A | 0.00 | 0.00 | 0.00 | 15 |
| MLTX-02-005-EM | Material Submittal for Pavement Markings | 15 | 100% | 100% | 02-May-26 | 18-May-26 | 19-Mar-26 A | 12-May-26 A | 0.00 | 0.00 | 0.00 | 5 |
| MLTX-02-005-EM | Material Approval for Pavement Markings | 15 | 100% | 100% | 19-May-26 | 08-Jun-26 | 26-Mar-26 A | 18-May-26 A | 0.00 | 0.00 | 0.00 | 15 |
| **TRAFFIC SIGNS** | | 30 | 0% | 0% | 02-May-26 | 08-Jun-26 | 19-Mar-26 A | 18-May-26 A | 0.00 | 0.00 | 0.00 | 15 |
| MLTX-02-005-EM | Material Submittal for Traffic Signs | 15 | 100% | 100% | 02-May-26 | 18-May-26 | 19-Mar-26 A | 12-May-26 A | 0.00 | 0.00 | 0.00 | 5 |
| MLTX-02-005-EM | Material Approval for Traffic Signs | 15 | 100% | 100% | 19-May-26 | 08-Jun-26 | 26-Mar-26 A | 18-May-26 A | 0.00 | 0.00 | 0.00 | 15 |
| **IRRIGATION PIPES/SPRINKLERS** | | 30 | 0% | 0% | 02-May-26 | 08-Jun-26 | 16-Jun-26 A | 18-Jun-26 A | 0.00 | 0.00 | 0.00 | -9 |
| MLTX-02-005-EM | Material Submittal for Irrigation Pipes/Sprinkles | 15 | 100% | 100% | 02-May-26 | 18-May-26 | 16-Jun-26 A | 16-Jun-26 A | 0.00 | 0.00 | 0.00 | -22 |
| MLTX-02-005-EM | Material Approval for Irrigation Pipes/Sprinkles | 15 | 100% | 100% | 19-May-26 | 08-Jun-26 | 18-Jun-26 A | 18-Jun-26 A | 0.00 | 0.00 | 0.00 | -9 |
| **AGRICULTURE SOIL** | | 30 | 0% | 0% | 02-May-26 | 08-Jun-26 | 19-Mar-26 A | 21-May-26 A | 0.00 | 0.00 | 0.00 | 12 |
| MLTX-02-005-EM | Material Submittal for Agriculture Soil | 15 | 100% | 100% | 02-May-26 | 18-May-26 | 19-Mar-26 A | 14-May-26 A | 0.00 | 0.00 | 0.00 | 3 |
| MLTX-02-005-EM | Material Approval for Agriculture Soil | 15 | 100% | 100% | 19-May-26 | 08-Jun-26 | 26-Mar-26 A | 21-May-26 A | 0.00 | 0.00 | 0.00 | 12 |
| **TRACK SURFACE** | | 30 | 0% | 0% | 02-May-26 | 08-Jun-26 | 19-Mar-26 A | 19-May-26 A | 0.00 | 0.00 | 0.00 | 14 |
| MLTX-02-005-EM | Material Submittal for Track Surface | 15 | 100% | 100% | 02-May-26 | 18-May-26 | 19-Mar-26 A | 14-May-26 A | 0.00 | 0.00 | 0.00 | 3 |
| MLTX-02-005-EM | Material Approval for Track Surface | 15 | 100% | 100% | 19-May-26 | 08-Jun-26 | 26-Mar-26 A | 19-May-26 A | 0.00 | 0.00 | 0.00 | 14 |
| **GRASS/TREES** | | 30 | 0% | 0% | 02-May-26 | 08-Jun-26 | 19-Mar-26 A | 21-May-26 A | 0.00 | 0.00 | 0.00 | 12 |
| MLTX-02-005-EM | Material Submittal for Grass/Trees | 15 | 100% | 100% | 02-May-26 | 18-May-26 | 19-Mar-26 A | 14-May-26 A | 0.00 | 0.00 | 0.00 | 3 |
| MLTX-02-005-EM | Material Approval for Grass/Trees | 15 | 100% | 100% | 19-May-26 | 08-Jun-26 | 26-Mar-26 A | 21-May-26 A | 0.00 | 0.00 | 0.00 | 12 |
| **CABLES** | | 30 | 0% | 0% | 02-May-26 | 08-Jun-26 | 19-Mar-26 A | 19-May-26 A | 0.00 | 0.00 | 0.00 | 14 |
| MLTX-02-005-EM | Material Submittal for Cables | 15 | 100% | 100% | 02-May-26 | 18-May-26 | 19-Mar-26 A | 14-May-26 A | 0.00 | 0.00 | 0.00 | 3 |
| MLTX-02-005-EM | Material Approval for Cables | 15 | 100% | 100% | 19-May-26 | 08-Jun-26 | 26-Mar-26 A | 19-May-26 A | 0.00 | 0.00 | 0.00 | 14 |
| **LIGHT POLES** | | 30 | 0% | 0% | 02-May-26 | 08-Jun-26 | 11-Jul-26 A | 11-Jul-26 A | 0.00 | 0.00 | 0.00 | -28 |
| MLTX-02-005-EM | Material Submittal for Lighting poles | 15 | 100% | 100% | 02-May-26 | 18-May-26 | 11-Jul-26 A | 11-Jul-26 A | 0.00 | 0.00 | 0.00 | -43 |
| MLTX-02-005-EM | Material Approval for Lighting poles | 15 | 100% | 100% | 19-May-26 | 08-Jun-26 | 11-Jul-26 A | 11-Jul-26 A | 0.00 | 0.00 | 0.00 | -28 |
| **PROCUREMENT** | | 183 | 0% | 0% | 19-May-26 | 22-Nov-26 | 02-Apr-26 A | 13-Feb-27 | 0.00 | 0.00 | 0.00 | -71 |
| **SHORT LEAD ITEM** | | 183 | 0% | 0% | 19-May-26 | 19-Oct-26 | 02-Apr-26 A | 13-Feb-27 | 0.00 | 0.00 | 0.00 | -100 |
| **TOILET/SERVICE WORKS** | | 94 | 0% | 0% | 19-May-26 | 09-Aug-26 | 02-Apr-26 A | 01-Nov-26 | 0.00 | 0.00 | 0.00 | -71 |
| **STEEL REINFORCEMENT** | | 54 | 0% | 0% | 19-May-26 | 02-Jun-26 | 02-Apr-26 A | 24-May-26 A | 0.00 | 0.00 | 0.00 | 5 |
| MLTX-02-005-PR-7 | PO for Steel Reinforcement | 5 | 100% | 100% | 19-May-26 | 24-May-26 | 02-Apr-26 A | 10-May-26 A | 0.00 | 0.00 | 0.00 | 12 |

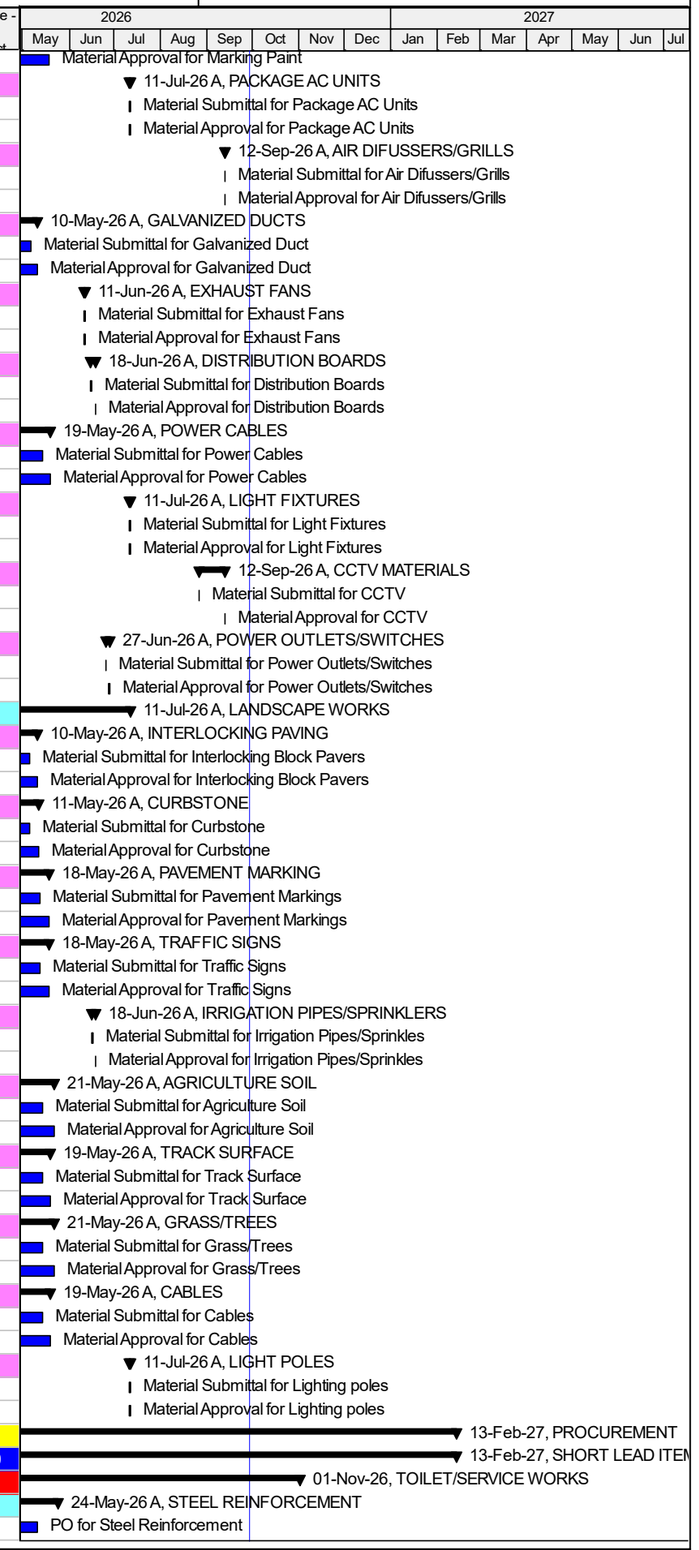


Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary




TASK filter: All Activities

© Oracle Corporation

# MLTX-02-005 - Playground Initiative for Eastern Region (Arar-Hasa osis -Dammam)

**Updateded schedule**
**D.D 28-09-2026**

| Activity ID | Activity Name | Original Duration | Schedule % Complete | Performance % Complete | BL Project Start | BL Project Finish | Start | Finish | Planned Value Cost | Earned Value Cost | Budgeted Total Cost | Variance - BL Project |
|---|---|---|---|---|---|---|---|---|---|---|---|---|
| MLTX-02-005-PR-7 | Material Delivery of Steel Reinforcement | 5 | 100% | 100% | 25-May-26 | 02-Jun-26 | 24-May-26 A | 24-May-26 A | 0.00 | 0.00 | 0.00 | 5 |
| **CONCRETE BLOCKS** | | 59 | 0% | 0% | 25-May-26 | 11-Jun-26 | 08-Apr-26 A | 07-Jul-26 A | 0.00 | 0.00 | 0.00 | -22 |
| MLTX-02-005-PR-7 | PO for Concrete Blocks | 5 | 100% | 100% | 25-May-26 | 02-Jun-26 | 08-Apr-26 A | 10-May-26 A | 0.00 | 0.00 | 0.00 | 17 |
| MLTX-02-005-PR-7 | Material Delivery of Concrete Blocks | 8 | 100% | 100% | 03-Jun-26 | 11-Jun-26 | 07-Jul-26 A | 07-Jul-26 A | 0.00 | 0.00 | 0.00 | -22 |
| **FLOOR/WALL TILES** | | 18 | 0% | 0% | 03-Jun-26 | 23-Jun-26 | 18-Aug-26 A | 20-Aug-26 A | 0.00 | 0.00 | 0.00 | -50 |
| MLTX-02-005-PR-8 | PO for Tilling Materials | 5 | 100% | 100% | 03-Jun-26 | 08-Jun-26 | 18-Aug-26 A | 18-Aug-26 A | 0.00 | 0.00 | 0.00 | -61 |
| MLTX-02-005-PR-8 | Material Delivery of Tailling Material | 13 | 100% | 100% | 09-Jun-26 | 23-Jun-26 | 20-Aug-26 A | 20-Aug-26 A | 0.00 | 0.00 | 0.00 | -50 |
| **SUSPENDED CEILING** | | 21 | 0% | 0% | 20-Jul-26 | 09-Aug-26 | 26-Jul-26 A | 20-Aug-26 A | 0.00 | 0.00 | 0.00 | -10 |
| MLTX-02-005-PR-8 | PO for Suspend Ceiling | 5 | 100% | 100% | 20-Jul-26 | 25-Jul-26 | 26-Jul-26 A | 26-Jul-26 A | 0.00 | 0.00 | 0.00 | -1 |
| MLTX-02-005-PR-8 | Material Delivery of Suspend Ceiling | 13 | 100% | 100% | 26-Jul-26 | 09-Aug-26 | 20-Aug-26 A | 20-Aug-26 A | 0.00 | 0.00 | 0.00 | -10 |
| **DOORS/WINDOWS** | | 20 | 0% | 0% | 09-Jun-26 | 01-Jul-26 | 15-Sep-26 A | 20-Sep-26 A | 0.00 | 0.00 | 0.00 | -69 |
| MLTX-02-005-PR-8 | PO for Doors/Windows | 5 | 100% | 100% | 09-Jun-26 | 14-Jun-26 | 15-Sep-26 A | 15-Sep-26 A | 0.00 | 0.00 | 0.00 | -80 |
| MLTX-02-005-PR-8 | Material Delivery for Doors/Windows | 15 | 100% | 100% | 15-Jun-26 | 01-Jul-26 | 20-Sep-26 A | 20-Sep-26 A | 0.00 | 0.00 | 0.00 | -69 |
| **WATER SUPPLY PIPES** | | 39 | 0% | 0% | 15-Jun-26 | 28-Jun-26 | 28-Apr-26 A | 07-Jul-26 A | 0.00 | 0.00 | 0.00 | -8 |
| MLTX-02-005-PR-8 | PO for Water Supply Pipes | 5 | 100% | 100% | 15-Jun-26 | 20-Jun-26 | 28-Apr-26 A | 03-May-26 A | 0.00 | 0.00 | 0.00 | 38 |
| MLTX-02-005-PR-8 | Material Delivery for Water Supply Pipes | 7 | 100% | 100% | 21-Jun-26 | 28-Jun-26 | 07-Jul-26 A | 07-Jul-26 A | 0.00 | 0.00 | 0.00 | -8 |
| **SEWAGE/DRAINAGE PIPES** | | 27 | 0% | 0% | 15-Jun-26 | 28-Jun-26 | 26-Apr-26 A | 07-Jul-26 A | 0.00 | 0.00 | 0.00 | -8 |
| MLTX-02-005-PR-8 | PO for Sewage/Drainage Pipes | 5 | 100% | 100% | 15-Jun-26 | 20-Jun-26 | 26-Apr-26 A | 10-May-26 A | 0.00 | 0.00 | 0.00 | 32 |
| MLTX-02-005-PR-8 | Material Delivery for Sewage/Drainage Pipes | 7 | 100% | 100% | 21-Jun-26 | 28-Jun-26 | 07-Jul-26 A | 07-Jul-26 A | 0.00 | 0.00 | 0.00 | -8 |
| **SANITARY FIXTURES** | | 31 | 0% | 0% | 21-Jun-26 | 11-Jul-26 | 28-Jul-26 A | 20-Aug-26 A | 0.00 | 0.00 | 0.00 | -35 |
| MLTX-02-005-PR-8 | PO for Sanitary Fixtures | 5 | 100% | 100% | 21-Jun-26 | 25-Jun-26 | 28-Jul-26 A | 28-Jul-26 A | 0.00 | 0.00 | 0.00 | -28 |
| MLTX-02-005-PR-8 | Material Delivery for Sanitary Fixtures | 13 | 100% | 100% | 27-Jun-26 | 11-Jul-26 | 20-Aug-26 A | 20-Aug-26 A | 0.00 | 0.00 | 0.00 | -35 |
| **PACKAGE AC UNITS** | | 20 | 0% | 0% | 27-Jun-26 | 19-Jul-26 | 07-Jul-26 A | 07-Jul-26 A | 0.00 | 0.00 | 0.00 | 10 |
| MLTX-02-005-PR-8 | PO for Package AC Units | 5 | 100% | 100% | 27-Jun-26 | 01-Jul-26 | 07-Jul-26 A | 07-Jul-26 A | 0.00 | 0.00 | 0.00 | -5 |
| MLTX-02-005-PR-8 | Material Delivery for Package AC Units | 15 | 100% | 100% | 02-Jul-26 | 19-Jul-26 | 07-Jul-26 A | 07-Jul-26 A | 0.00 | 0.00 | 0.00 | 10 |
| **AIR DIFUSSERS/GRILLS** | | 20 | 0% | 0% | 27-Jun-26 | 19-Jul-26 | 18-Aug-26 A | 20-Aug-26 A | 0.00 | 0.00 | 0.00 | -28 |
| MLTX-02-005-PR-8 | PO for Air Diffusers/Grills | 5 | 100% | 100% | 27-Jun-26 | 01-Jul-26 | 18-Aug-26 A | 18-Aug-26 A | 0.00 | 0.00 | 0.00 | -41 |
| MLTX-02-005-PR-8 | Material Delivery for Air Diffusers/Grills | 15 | 100% | 100% | 02-Jul-26 | 19-Jul-26 | 20-Aug-26 A | 20-Aug-26 A | 0.00 | 0.00 | 0.00 | -28 |
| **GALVANIZED DUCTS** | | 20 | 0% | 0% | 27-Jun-26 | 19-Jul-26 | 18-Aug-26 A | 20-Aug-26 A | 0.00 | 0.00 | 0.00 | -28 |
| MLTX-02-005-PR-8 | PO for Galvanized Ducts | 5 | 100% | 100% | 27-Jun-26 | 01-Jul-26 | 18-Aug-26 A | 18-Aug-26 A | 0.00 | 0.00 | 0.00 | -41 |
| MLTX-02-005-PR-8 | Material Delivery for Galvanized Ducts | 15 | 100% | 100% | 02-Jul-26 | 19-Jul-26 | 20-Aug-26 A | 20-Aug-26 A | 0.00 | 0.00 | 0.00 | -28 |
| **EXHAUST FANS** | | 15 | 0% | 0% | 27-Jun-26 | 13-Jul-26 | 20-Aug-26 A | 20-Aug-26 A | 0.00 | 0.00 | 0.00 | -33 |
| MLTX-02-005-PR-8 | PO for Exhaust Fans | 5 | 100% | 100% | 27-Jun-26 | 01-Jul-26 | 20-Aug-26 A | 20-Aug-26 A | 0.00 | 0.00 | 0.00 | -43 |
| MLTX-02-005-PR-8 | Material Delivery for Exhaust Fans | 10 | 100% | 100% | 02-Jul-26 | 13-Jul-26 | 20-Aug-26 A | 20-Aug-26 A | 0.00 | 0.00 | 0.00 | -33 |
| **LIGHTING FIXTURES** | | 30 | 0% | 0% | 02-Jul-26 | 19-Jul-26 | 07-Jul-26 A | 10-Oct-26 | 0.00 | 0.00 | 0.00 | -70 |
| MLTX-02-005-PR-8 | PO for Lighting Fixtures | 5 | 100% | 100% | 02-Jul-26 | 07-Jul-26 | 07-Jul-26 A | 07-Jul-26 A | 0.00 | 0.00 | 0.00 | 0 |
| MLTX-02-005-PR-8 | Material Delivery for Lighting Fixtures | 10 | 100% | 0% | 08-Jul-26 | 19-Jul-26 | 29-Sep-26 | 10-Oct-26 | 0.00 | 0.00 | 0.00 | -70 |
| **SWITCHES/SOCKETS** | | 12 | 0% | 0% | 08-Jul-26 | 21-Jul-26 | 29-Sep-26 | 12-Oct-26 | 0.00 | 0.00 | 0.00 | -70 |
| MLTX-02-005-PR-8 | PO for Switches/Sockets | 5 | 100% | 0% | 08-Jul-26 | 13-Jul-26 | 29-Sep-26 | 04-Oct-26 | 0.00 | 0.00 | 0.00 | -70 |
| MLTX-02-005-PR-8 | Material Delivery for Switches/Sockets | 7 | 100% | 0% | 14-Jul-26 | 21-Jul-26 | 05-Oct-26 | 12-Oct-26 | 0.00 | 0.00 | 0.00 | -70 |
| **EARTHING SYSTEM** | | 22 | 0% | 0% | 09-Jun-26 | 09-Jul-26 | 12-Jul-26 A | 12-Jul-26 A | 0.00 | 0.00 | 0.00 | -2 |
| MLTX-02-005-PR-8 | PO for Earthing System | 5 | 100% | 100% | 09-Jun-26 | 14-Jun-26 | 12-Jul-26 A | 12-Jul-26 A | 0.00 | 0.00 | 0.00 | -24 |
| MLTX-02-005-PR-8 | Material Delivery for Earthing System | 15 | 100% | 100% | 23-Jun-26 | 09-Jul-26 | 12-Jul-26 A | 12-Jul-26 A | 0.00 | 0.00 | 0.00 | -2 |
| **DISTRIBUTION PANNELS** | | 20 | 0% | 0% | 09-Jun-26 | 01-Jul-26 | 29-Sep-26 | 21-Oct-26 | 0.00 | 0.00 | 0.00 | -95 |
| MLTX-02-005-PR-8 | PO for Distribution Panels | 5 | 100% | 0% | 09-Jun-26 | 14-Jun-26 | 29-Sep-26 | 04-Oct-26 | 0.00 | 0.00 | 0.00 | -95 |
| MLTX-02-005-PR-8 | Material Delivery for Distribution Panels | 15 | 100% | 0% | 15-Jun-26 | 01-Jul-26 | 05-Oct-26 | 21-Oct-26 | 0.00 | 0.00 | 0.00 | -95 |
| **FURNITURES** | | 29 | 0% | 0% | 02-Jul-26 | 04-Aug-26 | 29-Sep-26 | 01-Nov-26 | 0.00 | 0.00 | 0.00 | -75 |
| MLTX-02-005-PR-8 | PO for Furnitures | 9 | 100% | 0% | 02-Jul-26 | 12-Jul-26 | 29-Sep-26 | 08-Oct-26 | 0.00 | 0.00 | 0.00 | -75 |
| MLTX-02-005-PR-8 | Material Delivery for Furnitures | 20 | 100% | 0% | 13-Jul-26 | 04-Aug-26 | 10-Oct-26 | 01-Nov-26 | 0.00 | 0.00 | 0.00 | -75 |
| **PLAYGROUND WORKS** | | 149 | 0% | 0% | 19-May-26 | 12-Sep-26 | 02-Apr-26 A | 25-Nov-26 | 0.00 | 0.00 | 0.00 | -63 |
| **PVC MEMBRANE** | | 21 | 0% | 0% | 13-Jun-26 | 18-Jul-26 | 02-Apr-26 A | 22-Oct-26 | 0.00 | 0.00 | 0.00 | -82 |
| MLTX-02-005-PR-8 | PO for PVC Membrane | 10 | 100% | 100% | 13-Jun-26 | 23-Jun-26 | 02-Apr-26 A | 19-May-26 A | 0.00 | 0.00 | 0.00 | 27 |
| MLTX-02-005-PR-8 | Material Delivery for PVC Membrane | 21 | 100% | 0% | 24-Jun-26 | 18-Jul-26 | 29-Sep-26 | 22-Oct-26 | 0.00 | 0.00 | 0.00 | -82 |
| **ARTIFICIAL TURF** | | 13 | 0% | 0% | 14-Jul-26 | 02-Aug-26 | 02-Apr-26 A | 05-Nov-26 | 0.00 | 0.00 | 0.00 | -81 |
| MLTX-02-005-PR-8 | PO for Artificial TURF | 5 | 100% | 100% | 14-Jul-26 | 19-Jul-26 | 02-Apr-26 A | 19-May-26 A | 0.00 | 0.00 | 0.00 | 49 |
| MLTX-02-005-PR-8 | Material Delivery for Artificial TURF | 12 | 100% | 0% | 20-Jul-26 | 02-Aug-26 | 24-Oct-26 | 05-Nov-26 | 0.00 | 0.00 | 0.00 | -81 |
| **RUBBER GRANULES** | | 12 | 0% | 0% | 13-Jun-26 | 01-Jul-26 | 02-Apr-26 A | 12-Oct-26 | 0.00 | 0.00 | 0.00 | -87 |
| MLTX-02-005-PR-8 | PO for Rubber Granules | 5 | 100% | 100% | 13-Jun-26 | 17-Jun-26 | 02-Apr-26 A | 19-May-26 A | 0.00 | 0.00 | 0.00 | 22 |
| MLTX-02-005-PR-8 | Material Delivery for Rubber Granules | 12 | 100% | 0% | 18-Jun-26 | 01-Jul-26 | 29-Sep-26 | 12-Oct-26 | 0.00 | 0.00 | 0.00 | -87 |
| **PADEL GLASS** | | 34 | 0% | 0% | 19-May-26 | 17-Jun-26 | 02-Apr-26 A | 19-Oct-26 | 0.00 | 0.00 | 0.00 | -105 |
| MLTX-02-005-PR-8 | PO for Padel Glass | 5 | 100% | 100% | 19-May-26 | 24-May-26 | 02-Apr-26 A | 19-May-26 A | 0.00 | 0.00 | 0.00 | 4 |
| MLTX-02-005-PR-8 | Material Delivery for Padel Glass | 18 | 100% | 0% | 25-May-26 | 17-Jun-26 | 29-Sep-26 | 19-Oct-26 | 0.00 | 0.00 | 0.00 | -105 |
| **PADEL WIRE MESH/STEEL SETS** | | 26 | 0% | 0% | 25-May-26 | 20-Jun-26 | 08-Apr-26 A | 15-Oct-26 | 0.00 | 0.00 | 0.00 | -100 |
| MLTX-02-005-PR-8 | PO for Wire Mesh/Steel Sets | 5 | 100% | 100% | 25-May-26 | 02-Jun-26 | 08-Apr-26 A | 19-May-26 A | 0.00 | 0.00 | 0.00 | 9 |

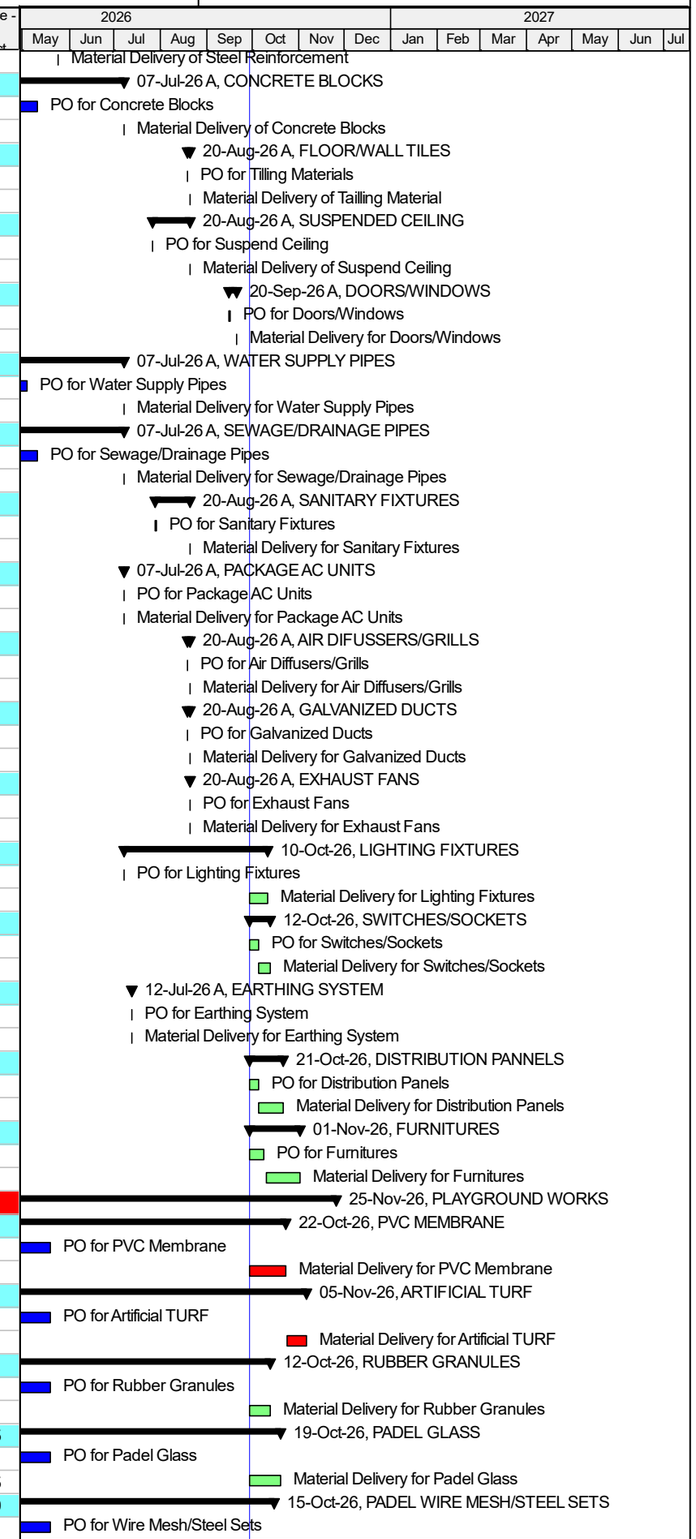


Actual Level of Effort | Remaining Work | Milestone
Actual Work | Critical Remaining Work | summary




TASK filter: All Activities

© Oracle Corporation

# MLTX-02-005 - Playground Initiative for Eastern Region (Arar-Hasa osis -Dammam)

**Updateded schedule**
**D.D 28-09-2026**

| Activity ID | Activity Name | Original Duration | Schedule % Complete | Performance % Complete | BL Project Start | BL Project Finish | Start | Finish | Planned Value Cost | Earned Value Cost | Budgeted Total Cost | Variance - BL Project |
|---|---|---|---|---|---|---|---|---|---|---|---|---|
| MLTX-02-005-PR-8 | Material Delivery for Wire Mesh/Steel Sets | 15 | 100% | 0% | 03-Jun-26 | 20-Jun-26 | 29-Sep-26 | 15-Oct-26 | 0.00 | 0.00 | 0.00 | -100 |
| **AGGREGATE BASE COURSE** | | 12 | 0% | 0% | 13-Jun-26 | 25-Jun-26 | 07-Jul-26 A | 07-Jul-26 A | 0.00 | 0.00 | 0.00 | -10 |
| MLTX-02-005-PR-8 | PO for Aggregate Base Course | 5 | 100% | 100% | 13-Jun-26 | 17-Jun-26 | 07-Jul-26 A | 07-Jul-26 A | 0.00 | 0.00 | 0.00 | -17 |
| MLTX-02-005-PR-8 | Material Delivery for Aggregate Base Course | 7 | 100% | 100% | 18-Jun-26 | 25-Jun-26 | 07-Jul-26 A | 07-Jul-26 A | 0.00 | 0.00 | 0.00 | -10 |
| **BITUMINOUS BASE & WEARING COURSE** | | 8 | 0% | 0% | 09-Jun-26 | 22-Jun-26 | 02-Apr-26 A | 06-Oct-26 | 0.00 | 0.00 | 0.00 | -90 |
| MLTX-02-005-PR-8 | PO for Bituminous Base & Wearing Course | 5 | 100% | 100% | 09-Jun-26 | 14-Jun-26 | 02-Apr-26 A | 14-May-26 A | 0.00 | 0.00 | 0.00 | 23 |
| MLTX-02-005-PR-8 | Material Delivery for the Site | 7 | 100% | 0% | 15-Jun-26 | 22-Jun-26 | 29-Sep-26 | 06-Oct-26 | 0.00 | 0.00 | 0.00 | -90 |
| **INTERLOCKING PAVING** | | 7 | 0% | 0% | 14-Jul-26 | 27-Jul-26 | 15-Sep-26 A | 14-Oct-26 | 0.00 | 0.00 | 0.00 | -67 |
| MLTX-02-005-PR-8 | PO for Interlocking Block Pavers | 5 | 100% | 100% | 14-Jul-26 | 19-Jul-26 | 15-Sep-26 A | 15-Sep-26 A | 0.00 | 0.00 | 0.00 | -50 |
| MLTX-02-005-PR-8 | Material Delivery for Interlocking Block Pavers | 7 | 100% | 0% | 20-Jul-26 | 27-Jul-26 | 07-Oct-26 | 14-Oct-26 | 0.00 | 0.00 | 0.00 | -67 |
| **MARKING PAINT** | | 12 | 0% | 0% | 15-Jun-26 | 28-Jun-26 | 29-Sep-26 | 12-Oct-26 | 0.00 | 0.00 | 0.00 | -90 |
| MLTX-02-005-PR-8 | PO for Marking Paint | 5 | 100% | 0% | 15-Jun-26 | 20-Jun-26 | 29-Sep-26 | 04-Oct-26 | 0.00 | 0.00 | 0.00 | -90 |
| MLTX-02-005-PR-8 | Material Delivery for Marking Paint | 7 | 100% | 0% | 21-Jun-26 | 28-Jun-26 | 05-Oct-26 | 12-Oct-26 | 0.00 | 0.00 | 0.00 | -90 |
| **PACKAGE AC UNITS** | | 20 | 0% | 0% | 03-Aug-26 | 25-Aug-26 | 04-Jul-26 A | 10-Jul-26 A | 0.00 | 0.00 | 0.00 | 40 |
| MLTX-02-005-PR-8 | PO for Package AC Units | 5 | 100% | 100% | 03-Aug-26 | 08-Aug-26 | 04-Jul-26 A | 04-Jul-26 A | 0.00 | 0.00 | 0.00 | 30 |
| MLTX-02-005-PR-8 | Material Delivery for Package AC Units | 15 | 100% | 100% | 09-Aug-26 | 25-Aug-26 | 10-Jul-26 A | 10-Jul-26 A | 0.00 | 0.00 | 0.00 | 40 |
| **AIR DIFUSSERS/GRILLS** | | 20 | 0% | 0% | 02-Jul-26 | 25-Jul-26 | 29-Sep-26 | 21-Oct-26 | 0.00 | 0.00 | 0.00 | -75 |
| MLTX-02-005-PR-8 | PO for Air Difussers/Grills | 5 | 100% | 0% | 02-Jul-26 | 07-Jul-26 | 29-Sep-26 | 04-Oct-26 | 0.00 | 0.00 | 0.00 | -75 |
| MLTX-02-005-PR-8 | Material Delivery for Air Difussers/Grills | 15 | 100% | 0% | 08-Jul-26 | 25-Jul-26 | 05-Oct-26 | 21-Oct-26 | 0.00 | 0.00 | 0.00 | -75 |
| **GALVANIZED DUCTS** | | 20 | 0% | 0% | 02-Jul-26 | 25-Jul-26 | 29-Sep-26 | 21-Oct-26 | 0.00 | 0.00 | 0.00 | -75 |
| MLTX-02-005-PR-8 | PO for Galvanized Duct | 5 | 100% | 0% | 02-Jul-26 | 07-Jul-26 | 29-Sep-26 | 04-Oct-26 | 0.00 | 0.00 | 0.00 | -75 |
| MLTX-02-005-PR-8 | Material Delivery for Galvanized Duct | 15 | 100% | 0% | 08-Jul-26 | 25-Jul-26 | 05-Oct-26 | 21-Oct-26 | 0.00 | 0.00 | 0.00 | -75 |
| **EXHAUST FANS** | | 20 | 0% | 0% | 02-Jul-26 | 25-Jul-26 | 29-Sep-26 | 21-Oct-26 | 0.00 | 0.00 | 0.00 | -75 |
| MLTX-02-005-PR-8 | PO for Exhaust Fans | 5 | 100% | 0% | 02-Jul-26 | 07-Jul-26 | 29-Sep-26 | 04-Oct-26 | 0.00 | 0.00 | 0.00 | -75 |
| MLTX-02-005-PR-8 | Material Delivery for Exhaust Fans | 15 | 100% | 0% | 08-Jul-26 | 25-Jul-26 | 05-Oct-26 | 21-Oct-26 | 0.00 | 0.00 | 0.00 | -75 |
| **DISTRIBUTION BOARDS** | | 20 | 0% | 0% | 02-Jul-26 | 25-Jul-26 | 17-Oct-26 | 08-Nov-26 | 0.00 | 0.00 | 0.00 | -90 |
| MLTX-02-005-PR-8 | PO for Distribution Boards | 5 | 100% | 0% | 02-Jul-26 | 07-Jul-26 | 17-Oct-26 | 21-Oct-26 | 0.00 | 0.00 | 0.00 | -90 |
| MLTX-02-005-PR-8 | Material Delivery for Distribution Boards | 15 | 100% | 0% | 08-Jul-26 | 25-Jul-26 | 22-Oct-26 | 08-Nov-26 | 0.00 | 0.00 | 0.00 | -90 |
| **POWER CABLES** | | 15 | 0% | 0% | 08-Jul-26 | 25-Jul-26 | 22-Oct-26 | 08-Nov-26 | 0.00 | 0.00 | 0.00 | -90 |
| MLTX-02-005-PR-8 | PO for Power Cables | 5 | 100% | 0% | 08-Jul-26 | 13-Jul-26 | 22-Oct-26 | 27-Oct-26 | 0.00 | 0.00 | 0.00 | -90 |
| MLTX-02-005-PR-8 | Material Delivery for Power Cables | 10 | 100% | 0% | 14-Jul-26 | 25-Jul-26 | 28-Oct-26 | 08-Nov-26 | 0.00 | 0.00 | 0.00 | -90 |
| **LIGHT FIXTURES** | | 45 | 0% | 0% | 14-Jul-26 | 30-Jul-26 | 07-Jul-26 A | 08-Nov-26 | 0.00 | 0.00 | 0.00 | -85 |
| MLTX-02-005-PR-8 | PO for Light Fixtures | 5 | 100% | 100% | 14-Jul-26 | 19-Jul-26 | 07-Jul-26 A | 07-Jul-26 A | 0.00 | 0.00 | 0.00 | 10 |
| MLTX-02-005-PR-8 | Material Delivery for Light Fixtures | 10 | 100% | 0% | 20-Jul-26 | 30-Jul-26 | 28-Oct-26 | 08-Nov-26 | 0.00 | 0.00 | 0.00 | -85 |
| **CCTV MATERIALS** | | 50 | 0% | 0% | 20-Jul-26 | 12-Sep-26 | 29-Sep-26 | 25-Nov-26 | 0.00 | 0.00 | 0.00 | -63 |
| MLTX-02-005-PR-8 | PO for CCTV | 5 | 100% | 0% | 20-Jul-26 | 25-Jul-26 | 29-Sep-26 | 04-Oct-26 | 0.00 | 0.00 | 0.00 | -60 |
| MLTX-02-005-PR-8 | Material Delivery for CCTV | 15 | 100% | 0% | 26-Aug-26 | 12-Sep-26 | 09-Nov-26 | 25-Nov-26 | 0.00 | 0.00 | 0.00 | -63 |
| **POWER OUTLETS/SWITCHES** | | 84 | 0% | 0% | 26-Jul-26 | 18-Aug-26 | 07-Jul-26 A | 15-Oct-26 | 0.00 | 0.00 | 0.00 | -49 |
| MLTX-02-005-PR-8 | PO for Power Outlets/Switches | 6 | 100% | 100% | 26-Jul-26 | 01-Aug-26 | 07-Jul-26 A | 07-Jul-26 A | 0.00 | 0.00 | 0.00 | 21 |
| MLTX-02-005-PR-8 | Material Delivery for Power Outlets/Switches | 15 | 100% | 0% | 02-Aug-26 | 18-Aug-26 | 29-Sep-26 | 15-Oct-26 | 0.00 | 0.00 | 0.00 | -49 |
| **LANDSCAPE WORKS** | | 118 | 0% | 0% | 02-Aug-26 | 19-Oct-26 | 16-May-26 A | 13-Feb-27 | 0.00 | 0.00 | 0.00 | -100 |
| **INTERLOCKING PAVING** | | 23 | 0% | 0% | 02-Aug-26 | 20-Aug-26 | 26-Aug-26 A | 26-Aug-26 A | 0.00 | 0.00 | 0.00 | -5 |
| MLTX-02-005-PR-8 | PO for Interlocking Block Pavers | 5 | 100% | 100% | 02-Aug-26 | 06-Aug-26 | 26-Aug-26 A | 26-Aug-26 A | 0.00 | 0.00 | 0.00 | -17 |
| MLTX-02-005-PR-8 | Material Delivery for Interlocking Block Pavers | 12 | 100% | 100% | 08-Aug-26 | 20-Aug-26 | 26-Aug-26 A | 26-Aug-26 A | 0.00 | 0.00 | 0.00 | -5 |
| **CURBSTONE** | | 17 | 0% | 0% | 02-Aug-26 | 20-Aug-26 | 28-Jul-26 A | 28-Jul-26 A | 0.00 | 0.00 | 0.00 | 20 |
| MLTX-02-005-PR-8 | PO for Curbstone | 5 | 100% | 100% | 02-Aug-26 | 06-Aug-26 | 28-Jul-26 A | 28-Jul-26 A | 0.00 | 0.00 | 0.00 | 8 |
| MLTX-02-005-PR-8 | Material Delivery for Curbstone | 12 | 100% | 100% | 08-Aug-26 | 20-Aug-26 | 28-Jul-26 A | 28-Jul-26 A | 0.00 | 0.00 | 0.00 | 20 |
| **PAVEMENT MARKING** | | 15 | 0% | 0% | 02-Aug-26 | 18-Aug-26 | 29-Sep-26 | 15-Oct-26 | 0.00 | 0.00 | 0.00 | -49 |
| MLTX-02-005-PR-8 | PO for Pavement Markings | 5 | 100% | 0% | 02-Aug-26 | 06-Aug-26 | 29-Sep-26 | 04-Oct-26 | 0.00 | 0.00 | 0.00 | -49 |
| MLTX-02-005-PR-8 | Material Delivery for Pavement Markings | 10 | 100% | 0% | 08-Aug-26 | 18-Aug-26 | 05-Oct-26 | 15-Oct-26 | 0.00 | 0.00 | 0.00 | -49 |
| **TRAFFIC SIGNS** | | 14 | 0% | 0% | 03-Oct-26 | 18-Oct-26 | 05-Oct-26 | 20-Oct-26 | 0.00 | 0.00 | 0.00 | -2 |
| MLTX-02-005-PR-8 | PO for Traffic Signs | 5 | 0% | 0% | 03-Oct-26 | 07-Oct-26 | 05-Oct-26 | 10-Oct-26 | 0.00 | 0.00 | 0.00 | -2 |
| MLTX-02-005-PR-8 | Material Delivery for Traffic Signs | 9 | 0% | 0% | 08-Oct-26 | 18-Oct-26 | 11-Oct-26 | 20-Oct-26 | 0.00 | 0.00 | 0.00 | -2 |
| **IRRIGATION PIPES/SPRINKLERS** | | 13 | 0% | 0% | 08-Aug-26 | 22-Aug-26 | 10-Jun-26 A | 02-Jul-26 A | 0.00 | 0.00 | 0.00 | 43 |
| MLTX-02-005-PR-8 | PO for Irrigation Pipes/Sprinkles | 5 | 100% | 100% | 08-Aug-26 | 12-Aug-26 | 10-Jun-26 A | 10-Jun-26 A | 0.00 | 0.00 | 0.00 | 54 |
| MLTX-02-005-PR-8 | Material Delivery for Irrigation Pipes/Sprinkles | 8 | 100% | 100% | 13-Aug-26 | 22-Aug-26 | 02-Jul-26 A | 02-Jul-26 A | 0.00 | 0.00 | 0.00 | 43 |
| **AGRICULTURE SOIL** | | 17 | 0% | 0% | 20-Sep-26 | 10-Oct-26 | 21-Jan-27 | 09-Feb-27 | 0.00 | 0.00 | 0.00 | -105 |
| MLTX-02-005-PR-8 | PO for Agriculture Soil | 5 | 100% | 0% | 20-Sep-26 | 26-Sep-26 | 21-Jan-27 | 26-Jan-27 | 0.00 | 0.00 | 0.00 | -105 |
| MLTX-02-005-PR-8 | Material Delivery for Agriculture Soil | 12 | 16.67% | 0% | 27-Sep-26 | 10-Oct-26 | 27-Jan-27 | 09-Feb-27 | 0.00 | 0.00 | 0.00 | -105 |
| **TRACK SURFACE** | | 26 | 0% | 0% | 02-Sep-26 | 19-Sep-26 | 16-May-26 A | 20-Jan-27 | 0.00 | 0.00 | 0.00 | -105 |
| MLTX-02-005-PR-8 | PO for Track Surface | 5 | 100% | 100% | 02-Sep-26 | 07-Sep-26 | 16-May-26 A | 19-May-26 A | 0.00 | 0.00 | 0.00 | 92 |
| MLTX-02-005-PR-8 | Material Delivery for Track Surface | 10 | 100% | 0% | 08-Sep-26 | 19-Sep-26 | 10-Jan-27 | 20-Jan-27 | 0.00 | 0.00 | 0.00 | -105 |
| **GRASS/TREES** | | 26 | 0% | 0% | 27-Sep-26 | 19-Oct-26 | 17-May-26 A | 13-Feb-27 | 0.00 | 0.00 | 0.00 | -100 |
| MLTX-02-005-PR-8 | PO for Grass/Trees | 5 | 40% | 100% | 27-Sep-26 | 01-Oct-26 | 17-May-26 A | 20-May-26 A | 0.00 | 0.00 | 0.00 | 111 |

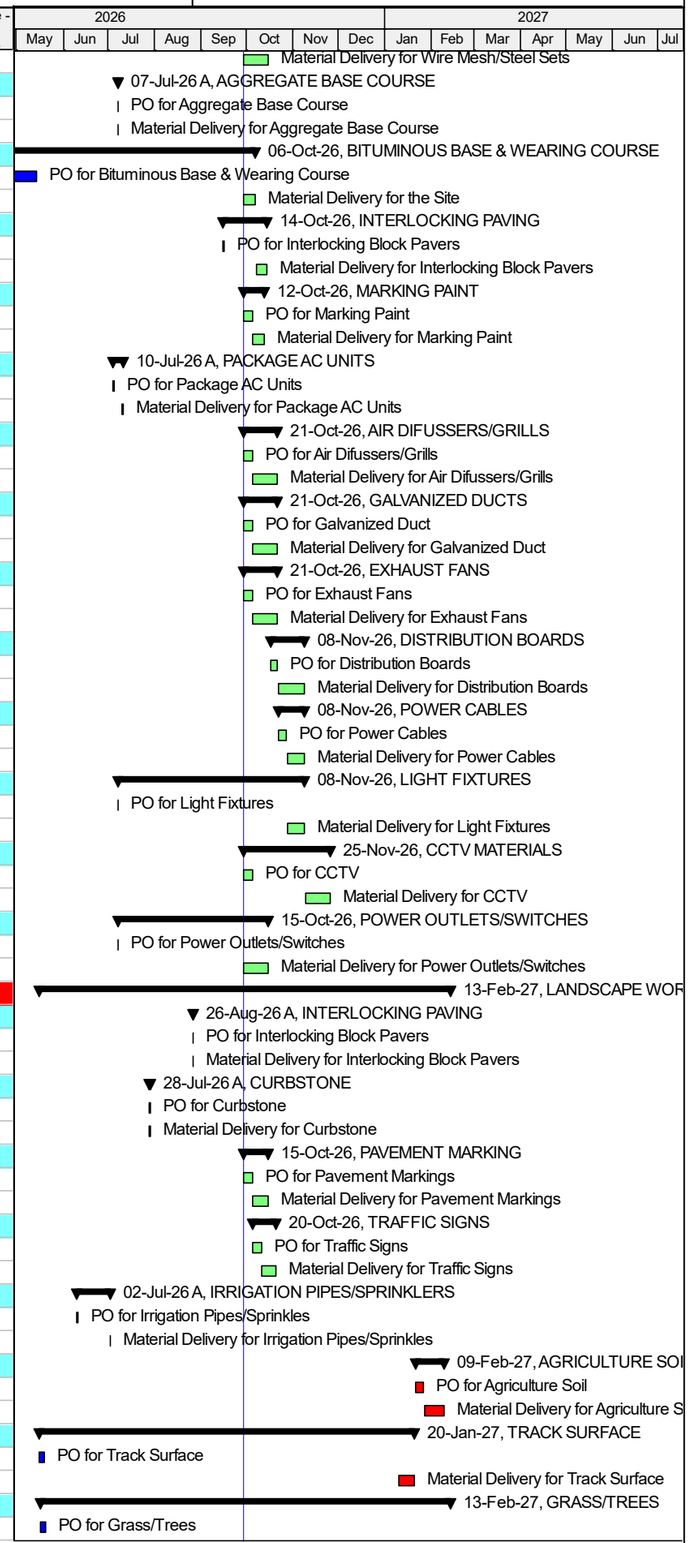


Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary




TASK filter: All Activities

© Oracle Corporation

# MLTX-02-005 - Playground Initiative for Eastern Region (Arar-Hasa osis -Dammam)

**Updateded schedule**
**D.D 28-09-2026**

| Activity ID | Activity Name | Original Duration | Schedule % Complete | Performance % Complete | BL Project Start | BL Project Finish | Start | Finish | Planned Value Cost | Earned Value Cost | Budgeted Total Cost | Variance - BL Project |
|---|---|---|---|---|---|---|---|---|---|---|---|---|
| MLTX-02-005-PR-9 | Material Delivery for Grass/Trees | 15 | 0% | 0% | 03-Oct-26 | 19-Oct-26 | 27-Jan-27 | 13-Feb-27 | 0.00 | 0.00 | 0.00 | -100 |
| **CABLES** | | 20 | 0% | 0% | 08-Aug-26 | 30-Aug-26 | 15-Sep-26 A | 15-Sep-26 A | 0.00 | 0.00 | 0.00 | -14 |
| MLTX-02-005-PR-9 | PO for Cables | 5 | 100% | 100% | 08-Aug-26 | 12-Aug-26 | 15-Sep-26 A | 15-Sep-26 A | 0.00 | 0.00 | 0.00 | -29 |
| MLTX-02-005-PR-9 | Material Delivery for Cables | 15 | 100% | 100% | 13-Aug-26 | 30-Aug-26 | 15-Sep-26 A | 15-Sep-26 A | 0.00 | 0.00 | 0.00 | -14 |
| **LONG LEAD ITEM** | | 109 | 0% | 0% | 19-May-26 | 22-Nov-26 | 07-Jul-26 A | 09-Jan-27 | 0.00 | 0.00 | 0.00 | -41 |
| **PLAYGROUND WORKS** | | 88 | 0% | 0% | 19-May-26 | 01-Sep-26 | 29-Sep-26 | 09-Jan-27 | 0.00 | 0.00 | 0.00 | -110 |
| **STEEL TENSION CABLES** | | 65 | 0% | 0% | 19-May-26 | 09-Aug-26 | 29-Sep-26 | 13-Dec-26 | 0.00 | 0.00 | 0.00 | -107 |
| MLTX-02-005-PR-8 | PO for Steel Tension Cables | 8 | 100% | 0% | 19-May-26 | 31-May-26 | 29-Sep-26 | 07-Oct-26 | 0.00 | 0.00 | 0.00 | -110 |
| MLTX-02-005-PR-8 | Material Fabrication for Steel Tension Cables | 20 | 100% | 0% | 01-Jun-26 | 23-Jun-26 | 08-Oct-26 | 31-Oct-26 | 0.00 | 0.00 | 0.00 | -110 |
| MLTX-02-005-PR-8 | Material Delivery for Steel Tension Cables | 30 | 100% | 0% | 28-Jun-26 | 01-Aug-26 | 01-Nov-26 | 05-Dec-26 | 0.00 | 0.00 | 0.00 | -107 |
| MLTX-02-005-PR-9 | Staging time | 7 | 100% | 0% | 02-Aug-26 | 09-Aug-26 | 06-Dec-26 | 13-Dec-26 | 0.00 | 0.00 | 0.00 | -107 |
| **EMERGENCY DOORS** | | 60 | 0% | 0% | 24-Jun-26 | 01-Sep-26 | 01-Nov-26 | 09-Jan-27 | 0.00 | 0.00 | 0.00 | -110 |
| MLTX-02-005-PR-8 | PO for Emergency Doors | 10 | 100% | 0% | 24-Jun-26 | 05-Jul-26 | 01-Nov-26 | 11-Nov-26 | 0.00 | 0.00 | 0.00 | -110 |
| MLTX-02-005-PR-8 | Material Fabrication for Emergency Doors | 20 | 100% | 0% | 06-Jul-26 | 28-Jul-26 | 12-Nov-26 | 05-Dec-26 | 0.00 | 0.00 | 0.00 | -110 |
| MLTX-02-005-PR-8 | Material Delivery for Emergency Doors | 25 | 100% | 0% | 29-Jul-26 | 26-Aug-26 | 06-Dec-26 | 03-Jan-27 | 0.00 | 0.00 | 0.00 | -110 |
| MLTX-02-005-PR-9 | Staging time | 5 | 100% | 0% | 27-Aug-26 | 01-Sep-26 | 04-Jan-27 | 09-Jan-27 | 0.00 | 0.00 | 0.00 | -110 |
| **PRESSURE UNITS** | | 60 | 0% | 0% | 24-Jun-26 | 01-Sep-26 | 01-Nov-26 | 09-Jan-27 | 0.00 | 0.00 | 0.00 | -110 |
| MLTX-02-005-PR-8 | PO for Pressure Units | 10 | 100% | 0% | 24-Jun-26 | 05-Jul-26 | 01-Nov-26 | 11-Nov-26 | 0.00 | 0.00 | 0.00 | -110 |
| MLTX-02-005-PR-8 | Material Fabrication for Pressure Units | 20 | 100% | 0% | 06-Jul-26 | 28-Jul-26 | 12-Nov-26 | 05-Dec-26 | 0.00 | 0.00 | 0.00 | -110 |
| MLTX-02-005-PR-8 | Material Delivery for Pressure Units | 25 | 100% | 0% | 29-Jul-26 | 26-Aug-26 | 06-Dec-26 | 03-Jan-27 | 0.00 | 0.00 | 0.00 | -110 |
| MLTX-02-005-PR-9 | Staging time | 5 | 100% | 0% | 27-Aug-26 | 01-Sep-26 | 04-Jan-27 | 09-Jan-27 | 0.00 | 0.00 | 0.00 | -110 |
| **AIR LOCK DOORS** | | 60 | 0% | 0% | 24-Jun-26 | 01-Sep-26 | 01-Nov-26 | 09-Jan-27 | 0.00 | 0.00 | 0.00 | -110 |
| MLTX-02-005-PR-8 | PO for Lock Doors | 10 | 100% | 0% | 24-Jun-26 | 05-Jul-26 | 01-Nov-26 | 11-Nov-26 | 0.00 | 0.00 | 0.00 | -110 |
| MLTX-02-005-PR-8 | Material Fabrication for Lock Doors | 20 | 100% | 0% | 06-Jul-26 | 28-Jul-26 | 12-Nov-26 | 05-Dec-26 | 0.00 | 0.00 | 0.00 | -110 |
| MLTX-02-005-PR-8 | Material Delivery for Lock Doors | 25 | 100% | 0% | 29-Jul-26 | 26-Aug-26 | 06-Dec-26 | 03-Jan-27 | 0.00 | 0.00 | 0.00 | -110 |
| MLTX-02-005-PR-9 | Staging time | 5 | 100% | 0% | 27-Aug-26 | 01-Sep-26 | 04-Jan-27 | 09-Jan-27 | 0.00 | 0.00 | 0.00 | -110 |
| **LANDSCAPE WORKS** | | 109 | 0% | 0% | 13-Aug-26 | 22-Nov-26 | 07-Jul-26 A | 20-Sep-26 A | 0.00 | 0.00 | 0.00 | 53 |
| **LIGHT POLES** | | 109 | 0% | 0% | 13-Aug-26 | 22-Nov-26 | 07-Jul-26 A | 20-Sep-26 A | 0.00 | 0.00 | 0.00 | 53 |
| MLTX-02-005-PR-9 | PO for Lighting poles | 10 | 100% | 100% | 13-Aug-26 | 24-Aug-26 | 07-Jul-26 A | 07-Jul-26 A | 0.00 | 0.00 | 0.00 | 41 |
| MLTX-02-005-PR-9 | Material Fabrication for Lighting poles | 30 | 43.33% | 100% | 13-Sep-26 | 18-Oct-26 | 26-Aug-26 A | 26-Aug-26 A | 0.00 | 0.00 | 0.00 | 44 |
| MLTX-02-005-PR-9 | Material Delivery for Lighting poles | 25 | 0% | 100% | 19-Oct-26 | 16-Nov-26 | 20-Sep-26 A | 20-Sep-26 A | 0.00 | 0.00 | 0.00 | 48 |
| MLTX-02-005-PR-9 | Staging time | 5 | 0% | 100% | 17-Nov-26 | 22-Nov-26 | 20-Sep-26 A | 20-Sep-26 A | 0.00 | 0.00 | 0.00 | 53 |
| **CONSTRUCTION PHASE** | | 238 | 30.37% | 30.96% | 15-Apr-26 | 02-Jan-27 | 04-Apr-26 A | 23-Mar-27 | 3,070,829.55 | 3,129,803.79 | 10,110,715.45 | -65 |
| **SITE WORKS** | | 238 | 21% | 29.46% | 15-Apr-26 | 02-Jan-27 | 04-Apr-26 A | 23-Mar-27 | 1,871,465.86 | 2,625,596.66 | 8,911,351.76 | -65 |
| **EARTH WORKS** | | 81 | 100% | 100% | 15-Apr-26 | 11-Jun-26 | 04-Apr-26 A | 05-Aug-26 A | 1,017,621.97 | 1,017,621.97 | 1,017,621.97 | -46 |
| MLTX-02-005-CN-993 | Excavation (in all types of soil) including Compaction | 12 | 100% | 100% | 02-May-26 | 14-May-26 | 06-Apr-26 A | 12-Apr-26 A | 180,460.75 | 180,460.75 | 180,460.75 | 29 |
| MLTX-02-005-CN-994 | Excavation (in all types of soil) including Compaction | 14 | 100% | 100% | 15-Apr-26 | 30-Apr-26 | 04-Apr-26 A | 02-Aug-26 A | 266,892.26 | 266,892.26 | 266,892.26 | -76 |
| MLTX-02-005-CN-995 | Excavation (in all types of soil) including Compaction | 7 | 100% | 100% | 16-May-26 | 23-May-26 | 28-Jun-26 A | 05-Aug-26 A | 243,701.49 | 243,701.49 | 243,701.49 | -60 |
| MLTX-02-005-CN-996 | Backfilling on Layers (Selected Soil) including Compaction | 21 | 100% | 100% | 16-May-26 | 11-Jun-26 | 13-Apr-26 A | 30-Apr-26 A | 117,028.93 | 117,028.93 | 117,028.93 | 34 |
| MLTX-02-005-CN-997 | Backfilling on Layers (Selected Soil) including Compaction | 20 | 100% | 100% | 02-May-26 | 24-May-26 | 06-Apr-26 A | 08-Apr-26 A | 60,984.78 | 60,984.78 | 60,984.78 | 39 |
| MLTX-02-005-CN-998 | Backfilling on Layers (Selected Soil) including Compaction | 8 | 100% | 100% | 24-May-26 | 04-Jun-26 | 21-Apr-26 A | 05-Aug-26 A | 148,553.76 | 148,553.76 | 148,553.76 | -52 |
| **LANDSCAPE WORKS** | | 205 | 10.9% | 20.3% | 13-Jun-26 | 02-Jan-27 | 17-May-26 A | 23-Mar-27 | 853,843.90 | 1,590,426.69 | 7,835,236.46 | -65 |
| **PLAYGROUND AREA** | | 194 | 36.23% | 50.77% | 13-Jun-26 | 02-Jan-27 | 19-May-26 A | 15-Mar-27 | 516,114.43 | 723,206.72 | 1,424,564.96 | -58 |
| **FOOTBALL PLAYGROUND** | | 182 | 35% | 35% | 13-Jun-26 | 01-Dec-26 | 19-May-26 A | 06-Mar-27 | 110,897.50 | 110,897.50 | 316,849.99 | -80 |
| MLTX-02-005-CI | Preparation and Proofing for Subgrade (Football Playground) | 20 | 100% | 100% | 13-Jun-26 | 05-Jul-26 | 19-May-26 A | 01-Jun-26 A | 79,212.50 | 79,212.50 | 79,212.50 | 29 |
| MLTX-02-005-CI | Backfilling and Compaction of Base Layers (Football | 21 | 100% | 100% | 06-Jul-26 | 29-Jul-26 | 01-Jun-26 A | 22-Jun-26 A | 15,842.50 | 15,842.50 | 15,842.50 | 33 |
| MLTX-02-005-CI | Finishing Asphalt & Concrete Surface (Football Playground) | 21 | 0% | 0% | 21-Oct-26 | 14-Nov-26 | 07-Nov-26 | 30-Nov-26 | 0.00 | 0.00 | 158,424.99 | -14 |
| MLTX-02-005-CI | Install Sport Equipments - Goal / Nets - (Football Playground) | 15 | 0% | 0% | 15-Nov-26 | 01-Dec-26 | 16-Feb-27 | 06-Mar-27 | 0.00 | 0.00 | 31,685.00 | -80 |
| MLTX-02-005-CI | Surface Marking and Painting Finishing Work (Football | 10 | 0% | 0% | 15-Nov-26 | 25-Nov-26 | 18-Jan-27 | 28-Jan-27 | 0.00 | 0.00 | 15,842.50 | -55 |
| MLTX-02-005-CI | Aggregate base course layer (Football Playground) | 21 | 100% | 100% | 30-Jul-26 | 23-Aug-26 | 02-Aug-26 A | 06-Aug-26 A | 15,842.50 | 15,842.50 | 15,842.50 | 14 |
| **PADEL PLAYGROUND** | | 189 | 45% | 70% | 06-Jul-26 | 01-Dec-26 | 19-May-26 A | 06-Mar-27 | 105,292.80 | 163,788.80 | 233,984.00 | -80 |
| MLTX-02-005-CI | Preparation and Proofing for Subgrade (Padel Playground) | 21 | 100% | 100% | 06-Jul-26 | 29-Jul-26 | 19-May-26 A | 01-Jun-26 A | 81,894.40 | 81,894.40 | 81,894.40 | 50 |
| MLTX-02-005-CI | Backfilling and Compaction of Base Layers (Padel | 21 | 100% | 100% | 30-Jul-26 | 23-Aug-26 | 01-Jun-26 A | 14-Jun-26 A | 11,699.20 | 11,699.20 | 11,699.20 | 61 |
| MLTX-02-005-CI | Finishing Asphalt & Concrete Surface (Padel Playground) | 21 | 0% | 100% | 21-Oct-26 | 14-Nov-26 | 29-Aug-26 A | 31-Aug-26 A | 0.00 | 58,496.00 | 58,496.00 | 64 |
| MLTX-02-005-CI | Install Sport Equipments - Goal / Nets - (Padel Playground) | 15 | 0% | 0% | 15-Nov-26 | 01-Dec-26 | 16-Feb-27 | 06-Mar-27 | 0.00 | 0.00 | 58,496.00 | -80 |
| MLTX-02-005-CI | Surface Marking and Painting Finishing Work (Padel | 10 | 0% | 0% | 15-Nov-26 | 25-Nov-26 | 16-Feb-27 | 28-Feb-27 | 0.00 | 0.00 | 11,699.20 | -80 |
| MLTX-02-005-CI | Aggregate base course layer (Padel Playground) | 21 | 100% | 100% | 24-Aug-26 | 16-Sep-26 | 15-Jun-26 A | 28-Jun-26 A | 11,699.20 | 11,699.20 | 11,699.20 | 70 |
| **BASKETBALL PLAYGROUND** | | 173 | 36.55% | 70% | 30-Jul-26 | 07-Dec-26 | 19-May-26 A | 15-Mar-27 | 118,139.79 | 226,230.90 | 323,187.00 | -80 |
| MLTX-02-005-CI | Preparation and Proofing for Subgrade (Basketball | 20 | 100% | 100% | 30-Jul-26 | 22-Aug-26 | 19-May-26 A | 01-Jun-26 A | 95,055.00 | 95,055.00 | 95,055.00 | 70 |
| MLTX-02-005-CI | Backfilling and Compaction of Base Layers (Basketball | 21 | 100% | 100% | 23-Aug-26 | 15-Sep-26 | 01-Jun-26 A | 14-Jun-26 A | 16,159.35 | 16,159.35 | 16,159.35 | 81 |
| MLTX-02-005-CI | Finishing Asphalt & Concrete Surface (Basketball | 21 | 0% | 100% | 13-Oct-26 | 05-Nov-26 | 19-Aug-26 A | 31-Aug-26 A | 0.00 | 98,857.20 | 98,857.20 | 57 |
| MLTX-02-005-CI | Install Sport Equipments - Goal / Nets - (Basketball | 15 | 0% | 0% | 15-Nov-26 | 01-Dec-26 | 16-Feb-27 | 06-Mar-27 | 0.00 | 0.00 | 80,796.75 | -80 |
| MLTX-02-005-CI | Surface Marking and Painting Finishing Work (Basketball | 10 | 0% | 0% | 26-Nov-26 | 07-Dec-26 | 01-Mar-27 | 15-Mar-27 | 0.00 | 0.00 | 16,159.35 | -80 |
| MLTX-02-005-CI | Aggregate base course layer (Basketball Playground) | 21 | 42.86% | 100% | 17-Sep-26 | 12-Oct-26 | 15-Jun-26 A | 28-Jun-26 A | 6,925.44 | 16,159.35 | 16,159.35 | 91 |

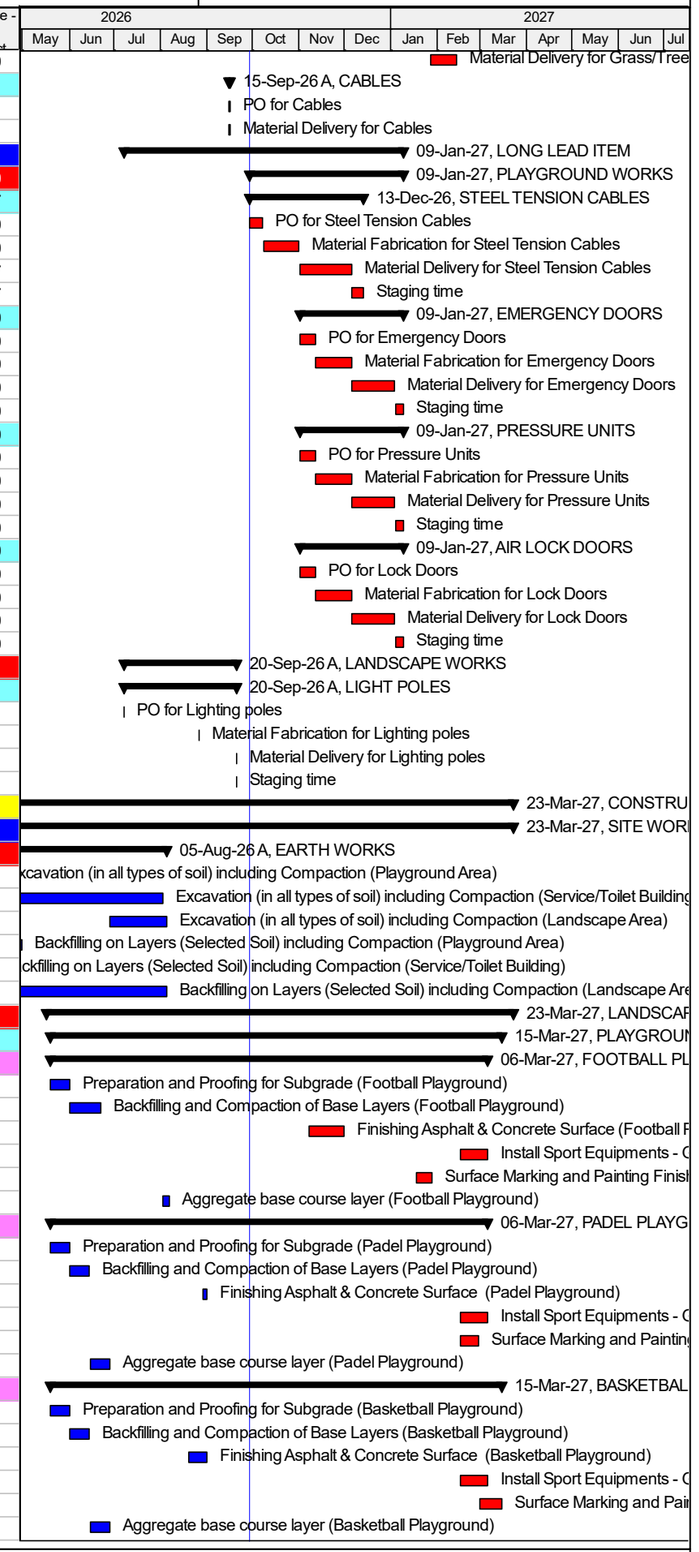


Actual Level of Effort | Remaining Work | Milestone
Actual Work | Critical Remaining Work | summary



TASK filter: All Activities

© Oracle Corporation

# MLTX-02-005 - Playground Initiative for Eastern Region (Arar-Hasa osis -Dammam)


**Updateded schedule**
**D.D 28-09-2026**

PROFAST شركة برو فاست المحدودة

egis

MODON مدن

| Activity ID | Activity Name | Original Duration | Schedule % Complete | Performance % Complete | BL Project Start | BL Project Finish | Start | Finish | Planned Value Cost | Earned Value Cost | Budgeted Total Cost | Variance - BL Project |
|---|---|---|---|---|---|---|---|---|---|---|---|---|
| **PADEL FENCE** | | 168 | 0% | 21.52% | 08-Dec-26 | 19-Dec-26 | 08-Aug-26 A | 10-Oct-26 | 0.00 | 40,505.18 | 188,238.96 | 60 |
| MLTX-02-005-CI | Excavation for Fence | 8 | 0% | 100% | 08-Dec-26 | 16-Dec-26 | 08-Aug-26 A | 08-Aug-26 A | 0.00 | 23,931.36 | 23,931.36 | 111 |
| MLTX-02-005-CI | Concrete Foundation for Fence including Posts Fixation | 7 | 0% | 100% | 08-Dec-26 | 15-Dec-26 | 15-Aug-26 A | 19-Aug-26 A | 0.00 | 16,573.82 | 16,573.82 | 100 |
| MLTX-02-005-CI | Backfilling and Reinstatement for Concrete Foundation | 7 | 0% | 0% | 08-Dec-26 | 15-Dec-26 | 29-Sep-26 | 06-Oct-26 | 0.00 | 0.00 | 4,143.45 | 60 |
| MLTX-02-005-CI | Tempered Glass Fenc Installation and Fixation | 10 | 0% | 0% | 08-Dec-26 | 19-Dec-26 | 29-Sep-26 | 10-Oct-26 | 0.00 | 0.00 | 33,147.63 | 60 |
| MLTX-02-005-CI | Chain Link Fence Installation and Fixation | 10 | 0% | 0% | 08-Dec-26 | 19-Dec-26 | 29-Sep-26 | 10-Oct-26 | 0.00 | 0.00 | 16,573.82 | 60 |
| MLTX-02-005-CI | Install of Fence Gates | 2 | 0% | 0% | 08-Dec-26 | 09-Dec-26 | 29-Sep-26 | 30-Sep-26 | 0.00 | 0.00 | 93,868.88 | 60 |
| **CURBSTOEN/INTERLOCK** | | 65 | 50.17% | 50.17% | 15-Sep-26 | 02-Jan-27 | 15-Aug-26 A | 08-Nov-26 | 181,784.34 | 181,784.34 | 362,305.01 | 47 |
| MLTX-02-005-CI | Interlock Installation (Grey Scale) for LandScape (Including | 20 | 0% | 0% | 10-Dec-26 | 02-Jan-27 | 17-Oct-26 | 08-Nov-26 | 0.00 | 0.00 | 180,520.67 | 47 |
| MLTX-02-005-CI | Concrete Works Under Curbstone | 7 | 100% | 100% | 15-Sep-26 | 22-Sep-26 | 15-Aug-26 A | 15-Aug-26 A | 54,535.30 | 54,535.30 | 54,535.30 | 33 |
| MLTX-02-005-CI | Curbstone Installation | 4 | 100% | 100% | 24-Sep-26 | 28-Sep-26 | 19-Aug-26 A | 05-Sep-26 A | 127,249.04 | 127,249.04 | 127,249.04 | 19 |
| **AIR DOME** | | 169 | 6.92% | 11.91% | 24-Aug-26 | 09-Dec-26 | 17-May-26 A | 23-Mar-27 | 337,729.47 | 581,544.30 | 4,881,359.87 | -85 |
| **CIVIL WORKS** | | 112 | 17.18% | 29.58% | 24-Aug-26 | 01-Nov-26 | 17-May-26 A | 27-Oct-26 | 337,729.47 | 581,544.30 | 1,966,294.68 | 4 |
| MLTX-02-005-CI | Excavation for Foundation (Air Dome) | 6 | 100% | 100% | 24-Aug-26 | 30-Aug-26 | 17-May-26 A | 31-May-26 A | 127,762.34 | 127,762.34 | 127,762.34 | 78 |
| MLTX-02-005-CI | Concrete Works for Foundations including Anchor Bolts (Air | 13 | 100% | 100% | 31-Aug-26 | 14-Sep-26 | 29-Jul-26 A | 21-Sep-26 A | 168,176.84 | 168,176.84 | 168,176.84 | -6 |
| MLTX-02-005-CI | Cable System Installation (Air Dome) | 5 | 100% | 100% | 15-Sep-26 | 20-Sep-26 | 21-Sep-26 A | 21-Sep-26 A | 41,790.29 | 41,790.29 | 41,790.29 | -1 |
| MLTX-02-005-CI | Install of Membrane Covering System (Air Dome) | 10 | 0% | 0% | 21-Oct-26 | 01-Nov-26 | 29-Sep-26 | 10-Oct-26 | 0.00 | 0.00 | 936,278.81 | 19 |
| MLTX-02-005-CI | Thermal Insulation Works (Air Dome) | 10 | 0% | 0% | 21-Oct-26 | 01-Nov-26 | 17-Oct-26 | 27-Oct-26 | 0.00 | 0.00 | 448,471.57 | 4 |
| MLTX-02-005-CI | Perimeter Clamping System Installation | 15 | 0% | 100% | 04-Oct-26 | 20-Oct-26 | 21-Sep-26 A | 28-Sep-26 A | 0.00 | 243,814.83 | 243,814.83 | 19 |
| **MECHANICAL WORKS** | | 76 | 0% | 0% | 02-Nov-26 | 16-Nov-26 | 28-Oct-26 | 24-Jan-27 | 0.00 | 0.00 | 1,233,296.81 | -59 |
| MLTX-02-005-CI | Air Ducts and Grills Installation (Air Dome) | 10 | 0% | 0% | 02-Nov-26 | 12-Nov-26 | 28-Oct-26 | 08-Nov-26 | 0.00 | 0.00 | 728,766.30 | 4 |
| MLTX-02-005-CI | Air Units Installation (Air Dome) | 13 | 0% | 0% | 02-Nov-26 | 16-Nov-26 | 10-Jan-27 | 24-Jan-27 | 0.00 | 0.00 | 336,353.67 | -59 |
| MLTX-02-005-CI | Exhaust Fans and Ducts Installation (Air Dome) | 7 | 0% | 0% | 02-Nov-26 | 09-Nov-26 | 10-Jan-27 | 17-Jan-27 | 0.00 | 0.00 | 168,176.84 | -59 |
| **ELECTRICAL WORKS** | | 20 | 0% | 0% | 17-Nov-26 | 09-Dec-26 | 25-Jan-27 | 16-Feb-27 | 0.00 | 0.00 | 1,513,591.54 | -59 |
| MLTX-02-005-CI | Light Fixture Works (Air Dome) | 6 | 0% | 0% | 17-Nov-26 | 23-Nov-26 | 25-Jan-27 | 31-Jan-27 | 0.00 | 0.00 | 224,235.78 | -59 |
| MLTX-02-005-CI | Distribution Board and Electrical Works (Air Dome) | 10 | 0% | 0% | 17-Nov-26 | 28-Nov-26 | 25-Jan-27 | 04-Feb-27 | 0.00 | 0.00 | 168,176.84 | -59 |
| MLTX-02-005-CI | External Electrical Connection Works (Air Dome) | 20 | 0% | 0% | 17-Nov-26 | 09-Dec-26 | 25-Jan-27 | 16-Feb-27 | 0.00 | 0.00 | 168,176.84 | -59 |
| MLTX-02-005-CI | Emergency Generator Installation (Air Dome) | 20 | 0% | 0% | 17-Nov-26 | 09-Dec-26 | 25-Jan-27 | 16-Feb-27 | 0.00 | 0.00 | 504,530.51 | -59 |
| MLTX-02-005-CI | Control System Installation (Air Dome) | 13 | 0% | 0% | 17-Nov-26 | 01-Dec-26 | 28-Jan-27 | 11-Feb-27 | 0.00 | 0.00 | 448,471.57 | -62 |
| **FINISHES WORKS** | | 49 | 0% | 0% | 14-Nov-26 | 09-Dec-26 | 21-Jan-27 | 23-Mar-27 | 0.00 | 0.00 | 168,176.84 | -85 |
| MLTX-02-005-CI | Doors Installation Including Emergency, Entrance doors (Air | 3 | 0% | 0% | 14-Nov-26 | 16-Nov-26 | 21-Jan-27 | 24-Jan-27 | 0.00 | 0.00 | 112,117.89 | -59 |
| MLTX-02-005-CI | Logo and Signs Installation (Air Dome) | 7 | 0% | 0% | 02-Dec-26 | 09-Dec-26 | 16-Mar-27 | 23-Mar-27 | 0.00 | 0.00 | 56,058.95 | -85 |
| **IRRIGATION NETWORK** | | 81 | 0% | 78.89% | 29-Sep-26 | 22-Oct-26 | 18-Aug-26 A | 16-Feb-27 | 0.00 | 120,240.42 | 152,414.87 | -100 |
| MLTX-02-005-CN-1 | Installing of HDPE Pipes for Irrigation Network (Main Line) | 4 | 0% | 100% | 29-Sep-26 | 03-Oct-26 | 18-Aug-26 A | 02-Sep-26 A | 0.00 | 53,620.00 | 53,620.00 | 25 |
| MLTX-02-005-CN-1 | Installing of HDPE Pipes for Irrigation Network (Branch Lines) | 4 | 0% | 100% | 04-Oct-26 | 07-Oct-26 | 03-Sep-26 A | 10-Sep-26 A | 0.00 | 50,127.83 | 50,127.83 | 22 |
| MLTX-02-005-CN-1 | Installing of Valves and fittings for Irrigation Network | 4 | 0% | 70% | 08-Oct-26 | 12-Oct-26 | 10-Sep-26 A | 03-Oct-26 | 0.00 | 16,492.59 | 23,560.84 | 8 |
| MLTX-02-005-CN-1 | Installing of Bubblers and Spreyers | 3 | 0% | 0% | 20-Oct-26 | 22-Oct-26 | 14-Feb-27 | 16-Feb-27 | 0.00 | 0.00 | 25,106.20 | -100 |
| **NATURAL GROUND** | | 81 | 0% | 0% | 13-Oct-26 | 22-Oct-26 | 15-Nov-26 | 16-Feb-27 | 0.00 | 0.00 | 191,740.00 | -100 |
| MLTX-02-005-CN-1 | Tartan Floor Installation Works for Landscape (Including | 3 | 0% | 0% | 20-Oct-26 | 22-Oct-26 | 14-Feb-27 | 16-Feb-27 | 0.00 | 0.00 | 126,740.00 | -100 |
| MLTX-02-005-CN-1 | Compacted Natural Ground Soil Installation Works for | 6 | 0% | 0% | 13-Oct-26 | 19-Oct-26 | 15-Nov-26 | 21-Nov-26 | 0.00 | 0.00 | 65,000.00 | -28 |
| **PLANTING** | | 24 | 0% | 0% | 24-Oct-26 | 19-Nov-26 | 17-Feb-27 | 21-Mar-27 | 0.00 | 0.00 | 347,251.46 | -100 |
| MLTX-02-005-CN-1 | Placement of Sweet/Agricultural Soil (Including Levelling and | 10 | 0% | 0% | 24-Oct-26 | 03-Nov-26 | 17-Feb-27 | 01-Mar-27 | 0.00 | 0.00 | 104,175.44 | -100 |
| MLTX-02-005-CN-1 | Placement of Lawn Ground Cover (Rolling and Compaction) | 3 | 0% | 0% | 17-Nov-26 | 19-Nov-26 | 18-Mar-27 | 21-Mar-27 | 0.00 | 0.00 | 141,732.50 | -100 |
| MLTX-02-005-CN-1 | Placement and Fixation of Trees | 11 | 0% | 0% | 04-Nov-26 | 16-Nov-26 | 02-Mar-27 | 17-Mar-27 | 0.00 | 0.00 | 101,343.52 | -100 |
| **WALKING/BIKE PATHS** | | 12 | 0% | 45% | 21-Nov-26 | 03-Dec-26 | 11-Jun-26 A | 29-Sep-26 | 0.00 | 165,435.26 | 367,633.90 | 57 |
| MLTX-02-005-CN-1 | Bike Path Preparation and Installation Works | 12 | 0% | 45% | 21-Nov-26 | 03-Dec-26 | 11-Jun-26 A | 29-Sep-26 | 0.00 | 84,399.35 | 187,554.12 | 57 |
| MLTX-02-005-CN-1 | Walking Path Preparation and Installation Works | 12 | 0% | 45% | 21-Nov-26 | 03-Dec-26 | 11-Jun-26 A | 29-Sep-26 | 0.00 | 81,035.90 | 180,079.78 | 57 |
| **GENERAL/FURNITURE** | | 27 | 0% | 0% | 29-Sep-26 | 02-Jan-27 | 29-Sep-26 | 29-Oct-26 | 0.00 | 0.00 | 470,271.40 | 55 |
| MLTX-02-005-CN-1 | Stamped Concrete Works for LandScape (Including | 5 | 0% | 0% | 05-Dec-26 | 09-Dec-26 | 29-Sep-26 | 04-Oct-26 | 0.00 | 0.00 | 93,594.00 | 57 |
| MLTX-02-005-CN-1 | Traffic Signs Posts and Poles Installation | 7 | 0% | 0% | 26-Dec-26 | 02-Jan-27 | 22-Oct-26 | 29-Oct-26 | 0.00 | 0.00 | 9,749.30 | 55 |
| MLTX-02-005-CN-1 | Fixation and Installation of Steel Frame for Benches | 7 | 0% | 0% | 05-Dec-26 | 12-Dec-26 | 29-Sep-26 | 06-Oct-26 | 0.00 | 0.00 | 17,274.79 | 57 |
| MLTX-02-005-CN-1 | Fixation and Installation of Benches | 7 | 0% | 0% | 13-Dec-26 | 20-Dec-26 | 07-Oct-26 | 14-Oct-26 | 0.00 | 0.00 | 40,307.84 | 57 |
| MLTX-02-005-CN-1 | Fixation and Installation of Precast Concrete Seats | 7 | 0% | 0% | 13-Dec-26 | 20-Dec-26 | 07-Oct-26 | 14-Oct-26 | 0.00 | 0.00 | 32,757.76 | 57 |
| MLTX-02-005-CN-1 | Fixation and Installation of Precast Concrete Seats (Circular) | 7 | 0% | 0% | 13-Dec-26 | 20-Dec-26 | 07-Oct-26 | 14-Oct-26 | 0.00 | 0.00 | 12,869.04 | 57 |
| MLTX-02-005-CN-1 | Fixation and Installation of Precast Concrete Trash Bins | 11 | 0% | 0% | 21-Dec-26 | 02-Jan-27 | 15-Oct-26 | 27-Oct-26 | 0.00 | 0.00 | 12,186.67 | 57 |
| MLTX-02-005-CN-1 | Preleminary Works for Site Light Poles Including Cable and | 7 | 0% | 0% | 29-Sep-26 | 06-Oct-26 | 29-Sep-26 | 06-Oct-26 | 0.00 | 0.00 | 75,459.60 | 0 |
| MLTX-02-005-CN-1 | Installing of Site Light Poles | 13 | 0% | 0% | 10-Dec-26 | 24-Dec-26 | 07-Oct-26 | 21-Oct-26 | 0.00 | 0.00 | 176,072.40 | 55 |
| **PARKING** | | 159 | 0% | 30% | 10-Dec-26 | 16-Dec-26 | 16-May-26 A | 01-Oct-26 | 0.00 | 17,548.00 | 58,493.33 | 65 |
| MLTX-02-005-CN-106 | Interlock Installation (8 Cm) for Parking Area (Including | 3 | 0% | 0% | 14-Dec-26 | 16-Dec-26 | 29-Sep-26 | 01-Oct-26 | 0.00 | 0.00 | 40,945.33 | 65 |
| MLTX-02-005-CN-107 | Site Preparation & Compaction Under Interlock for Parking | 3 | 0% | 100% | 10-Dec-26 | 13-Dec-26 | 16-May-26 A | 22-Jul-26 A | 0.00 | 17,548.00 | 17,548.00 | 123 |
| **TOILET/SERVICE BUILDING** | | 123 | 100% | 42.04% | 06-Jun-26 | 26-Sep-26 | 21-May-26 A | 30-Nov-26 | 1,199,363.69 | 504,207.13 | 1,199,363.69 | -56 |
| **STRUCTURE WORKS** | | 98 | 100% | 100% | 06-Jun-26 | 27-Jul-26 | 21-May-26 A | 02-Aug-26 A | 194,188.64 | 194,188.64 | 194,188.64 | -5 |
| **CONCRETE WORKS** | | 86 | 100% | 100% | 25-Jun-26 | 27-Jul-26 | 20-Jun-26 A | 12-Jul-26 A | 134,099.30 | 134,099.30 | 134,099.30 | 13 |
| **SUB-STRUCTURE** | | 86 | 100% | 100% | 25-Jun-26 | 05-Jul-26 | 20-Jun-26 A | 25-Jun-26 A | 53,666.80 | 53,666.80 | 53,666.80 | 8 |

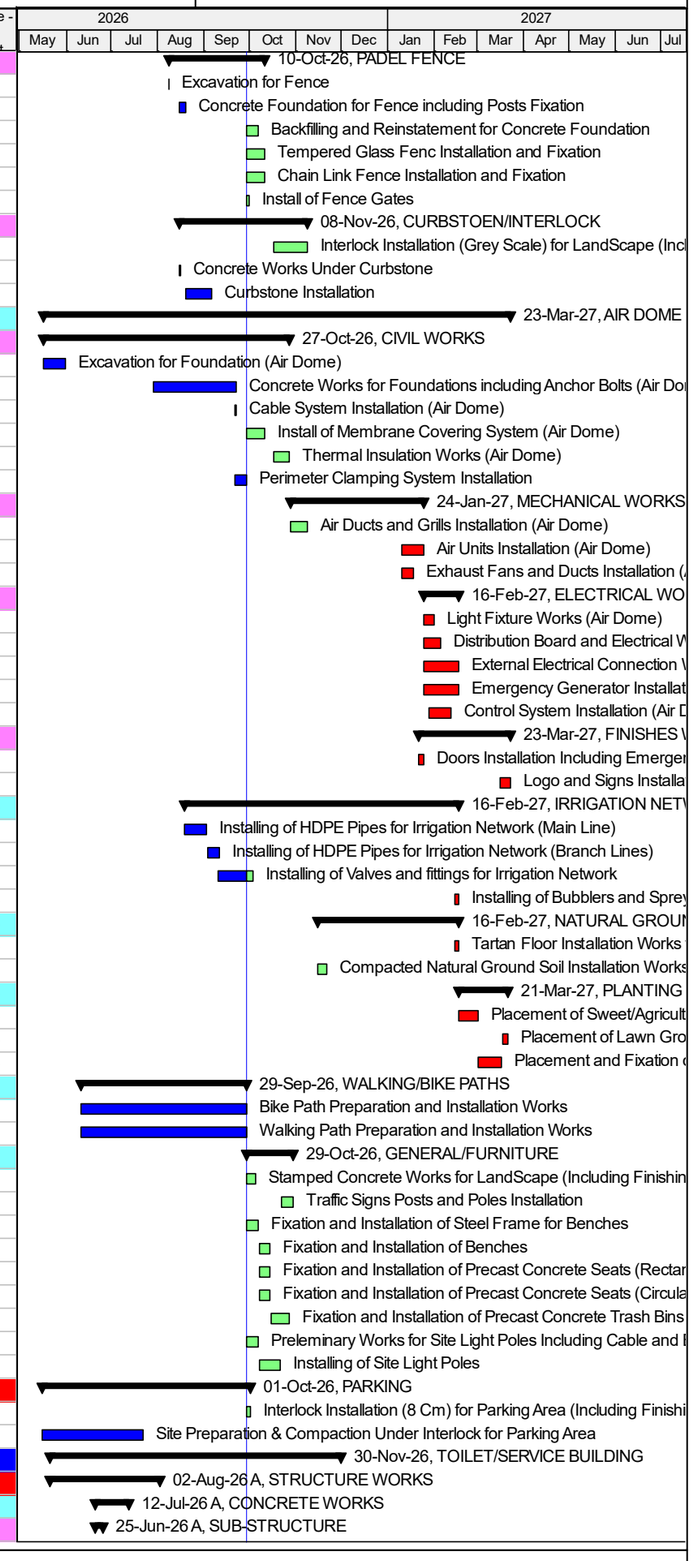


Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary




TASK filter: All Activities

© Oracle Corporation

# MLTX-02-005 - Playground Initiative for Eastern Region (Arar-Hasa osis -Dammam)

**Updateded schedule**
**D.D 28-09-2026**

| Activity ID | Activity Name | Original Duration | Schedule % Complete | Performance % Complete | BL Project Start | BL Project Finish | Start | Finish | Planned Value Cost | Earned Value Cost | Budgeted Total Cost | Variance - BL Project |
|---|---|---|---|---|---|---|---|---|---|---|---|---|
| MLTX-02-005-CI | Plain Concrete Under Footing | 4 | 100% | 100% | 25-Jun-26 | 29-Jun-26 | 20-Jun-26 A | 21-Jun-26 A | 17,106.85 | 17,106.85 | 17,106.85 | 7 |
| MLTX-02-005-CI | Reinforced Concrete Works for Slab on Grade Including | 5 | 100% | 100% | 30-Jun-26 | 05-Jul-26 | 22-Jun-26 A | 25-Jun-26 A | 36,559.95 | 36,559.95 | 36,559.95 | 8 |
| **SUPER-STRUCTURE** | | 10 | 100% | 100% | 12-Jul-26 | 27-Jul-26 | 07-Jul-26 A | 12-Jul-26 A | 80,432.50 | 80,432.50 | 80,432.50 | 13 |
| MLTX-02-005-CI | AAC Panels Works for Walls | 7 | 100% | 100% | 12-Jul-26 | 19-Jul-26 | 07-Jul-26 A | 08-Jul-26 A | 48,259.50 | 48,259.50 | 48,259.50 | 9 |
| MLTX-02-005-CI | AAC Panels Works for Slabs | 3 | 100% | 100% | 20-Jul-26 | 22-Jul-26 | 09-Jul-26 A | 11-Jul-26 A | 16,086.50 | 16,086.50 | 16,086.50 | 10 |
| MLTX-02-005-CI | Parpet Works and Lintels | 4 | 100% | 100% | 23-Jul-26 | 27-Jul-26 | 11-Jul-26 A | 12-Jul-26 A | 16,086.50 | 16,086.50 | 16,086.50 | 13 |
| **UNDER GROUND SEPTIC TANK** | | 32 | 100% | 100% | 07-Jun-26 | 13-Jul-26 | 31-May-26 A | 24-Jun-26 A | 49,852.54 | 49,852.54 | 49,852.54 | 16 |
| MLTX-02-005-CN-1 | Plain Concrete Under Footing | 3 | 100% | 100% | 07-Jun-26 | 09-Jun-26 | 31-May-26 A | 01-Jun-26 A | 17,106.85 | 17,106.85 | 17,106.85 | 7 |
| MLTX-02-005-CN-1 | Reinforced Concrete Works for Tank Foundation Including | 8 | 100% | 100% | 10-Jun-26 | 18-Jun-26 | 10-Jun-26 A | 13-Jun-26 A | 7,604.46 | 7,604.46 | 7,604.46 | 5 |
| MLTX-02-005-CN-1 | Reinforced Concrete Works for Tank Walls Including Steel | 11 | 100% | 100% | 20-Jun-26 | 01-Jul-26 | 07-Jun-26 A | 11-Jun-26 A | 16,366.86 | 16,366.86 | 16,366.86 | 17 |
| MLTX-02-005-CN-1 | Reinforced Concrete Works for Tank Slab Including | 10 | 100% | 100% | 02-Jul-26 | 13-Jul-26 | 20-Jun-26 A | 24-Jun-26 A | 8,774.37 | 8,774.37 | 8,774.37 | 16 |
| **THERMAL & MOISTER PROTECTION** | | 74 | 100% | 100% | 06-Jun-26 | 22-Jul-26 | 21-May-26 A | 02-Aug-26 A | 10,236.80 | 10,236.80 | 10,236.80 | -9 |
| **ANTI TERMIT CONTROL** | | 13 | 100% | 100% | 06-Jun-26 | 20-Jun-26 | 21-May-26 A | 25-May-26 A | 4,387.50 | 4,387.50 | 4,387.50 | 19 |
| MLTX-02-005-CI | Anti Termite Works Under Foundation | 1 | 100% | 100% | 06-Jun-26 | 06-Jun-26 | 24-May-26 A | 25-May-26 A | 1,755.00 | 1,755.00 | 1,755.00 | 7 |
| MLTX-02-005-CI | Anti Termite Works Under Slab on Grade and Grade Beams | 1 | 100% | 100% | 20-Jun-26 | 20-Jun-26 | 21-May-26 A | 21-May-26 A | 2,632.50 | 2,632.50 | 2,632.50 | 23 |
| **POLYETHYLENE SHEET** | | 62 | 100% | 100% | 06-Jun-26 | 20-Jun-26 | 25-May-26 A | 21-Jun-26 A | 2,193.30 | 2,193.30 | 2,193.30 | -1 |
| MLTX-02-005-CI | Water Proofing Under Blinding Concrete (Polythelen Sheet) | 1 | 100% | 100% | 06-Jun-26 | 06-Jun-26 | 25-May-26 A | 31-May-26 A | 877.32 | 877.32 | 877.32 | 5 |
| MLTX-02-005-CI | Water Proofing Under Slab on Grade (Polythelen Sheet) | 1 | 100% | 100% | 20-Jun-26 | 20-Jun-26 | 21-Jun-26 A | 21-Jun-26 A | 1,315.98 | 1,315.98 | 1,315.98 | -1 |
| **EPOXY** | | 8 | 100% | 100% | 14-Jul-26 | 22-Jul-26 | 12-Jul-26 A | 02-Aug-26 A | 3,656.00 | 3,656.00 | 3,656.00 | -9 |
| MLTX-02-005-CI | Surface Preparation for Epoxy Coating | 3 | 100% | 100% | 14-Jul-26 | 16-Jul-26 | 12-Jul-26 A | 12-Jul-26 A | 1,096.80 | 1,096.80 | 1,096.80 | 4 |
| MLTX-02-005-CI | Epoxy Coating for Walls and Slab of Tank | 5 | 100% | 100% | 18-Jul-26 | 22-Jul-26 | 25-Jul-26 A | 02-Aug-26 A | 2,559.20 | 2,559.20 | 2,559.20 | -9 |
| **MASONARY WORK** | | 5 | 100% | 100% | 06-Jul-26 | 11-Jul-26 | 13-Jul-26 A | 14-Jul-26 A | 12,284.10 | 12,284.10 | 12,284.10 | -3 |
| MLTX-02-005-CN-11C | CMU Masonary Works Including all Accessories | 5 | 100% | 100% | 06-Jul-26 | 11-Jul-26 | 13-Jul-26 A | 14-Jul-26 A | 12,284.10 | 12,284.10 | 12,284.10 | -3 |
| **THERMAL & MOISTER PROTECTION** | | 21 | 100% | 6.07% | 28-Jul-26 | 20-Aug-26 | 26-Sep-26 A | 20-Oct-26 | 34,698.32 | 2,105.86 | 34,698.32 | -51 |
| MLTX-02-005-CN-11C | Preparing Surface and Preliminary Works for Toilets | 2 | 100% | 100% | 28-Jul-26 | 29-Jul-26 | 26-Sep-26 A | 26-Sep-26 A | 2,105.86 | 2,105.86 | 2,105.86 | -49 |
| MLTX-02-005-CN-11C | Preparing Surface and Preliminary Works for Roofing and | 5 | 100% | 0% | 06-Aug-26 | 11-Aug-26 | 06-Oct-26 | 11-Oct-26 | 11,071.52 | 0.00 | 11,071.52 | -51 |
| MLTX-02-005-CN-11C | Finalize Water Proofing Works for Toilets | 6 | 100% | 0% | 30-Jul-26 | 05-Aug-26 | 29-Sep-26 | 05-Oct-26 | 4,913.66 | 0.00 | 4,913.66 | -51 |
| MLTX-02-005-CN-11C | Finalize Water Proofing Works for Roofing and Wet Areas | 8 | 100% | 0% | 12-Aug-26 | 20-Aug-26 | 12-Oct-26 | 20-Oct-26 | 16,607.28 | 0.00 | 16,607.28 | -51 |
| **MECHANICAL WORK** | | 57 | 100% | 16.98% | 06-Aug-26 | 21-Sep-26 | 18-Jul-26 A | 12-Nov-26 | 264,673.10 | 44,947.89 | 264,673.10 | -44 |
| **HVAC SYSTEM** | | 52 | 100% | 47.55% | 20-Aug-26 | 20-Sep-26 | 19-Jul-26 A | 11-Nov-26 | 27,883.37 | 13,259.41 | 27,883.37 | -44 |
| MLTX-02-005-CN-1 | Preliminary HVAC and Ventilation Works | 3 | 100% | 100% | 20-Aug-26 | 23-Aug-26 | 19-Jul-26 A | 22-Jul-26 A | 9,359.69 | 9,359.69 | 9,359.69 | 27 |
| MLTX-02-005-CN-1 | Exhaust, Air Ducts Installation with all Accessories | 6 | 100% | 100% | 24-Aug-26 | 30-Aug-26 | 12-Sep-26 A | 12-Sep-26 A | 3,899.72 | 3,899.72 | 3,899.72 | -11 |
| MLTX-02-005-CN-1 | Install and Finish HVAC and Ventilation Works Including Split | 3 | 100% | 0% | 17-Sep-26 | 20-Sep-26 | 09-Nov-26 | 11-Nov-26 | 14,623.96 | 0.00 | 14,623.96 | -44 |
| **WATER SUPPLY SYSTEM** | | 50 | 100% | 12.86% | 09-Aug-26 | 13-Sep-26 | 28-Jul-26 A | 04-Nov-26 | 154,916.69 | 19,921.08 | 154,916.69 | -44 |
| MLTX-02-005-CN-1 | Installing of Valves and Fittings | 2 | 100% | 100% | 12-Aug-26 | 13-Aug-26 | 05-Sep-26 A | 05-Sep-26 A | 6,499.60 | 6,499.60 | 6,499.60 | -19 |
| MLTX-02-005-CN-1 | Installing of HDPE Pipes and Valves for Water Supply | 3 | 100% | 0% | 15-Aug-26 | 17-Aug-26 | 29-Sep-26 | 01-Oct-26 | 25,998.40 | 0.00 | 25,998.40 | -38 |
| MLTX-02-005-CN-1 | Installing of PPR Pipes and Fittings for Water Network | 3 | 100% | 100% | 09-Aug-26 | 11-Aug-26 | 28-Jul-26 A | 02-Aug-26 A | 6,921.94 | 6,921.94 | 6,921.94 | 8 |
| MLTX-02-005-CN-1 | Installing of Booster Pump Units Including fittings and | 7 | 100% | 0% | 02-Sep-26 | 09-Sep-26 | 08-Oct-26 | 15-Oct-26 | 48,746.52 | 0.00 | 48,746.52 | -30 |
| MLTX-02-005-CN-1 | Installing of GRP Tanks | 8 | 100% | 10% | 24-Aug-26 | 01-Sep-26 | 28-Sep-26 A | 07-Oct-26 | 64,995.36 | 6,499.54 | 64,995.36 | -30 |
| MLTX-02-005-CN-1 | Installing of Water Heater | 4 | 100% | 0% | 09-Sep-26 | 13-Sep-26 | 01-Nov-26 | 04-Nov-26 | 1,754.87 | 0.00 | 1,754.87 | -44 |
| **SEWER/DRAINAGE SYSTEM** | | 46 | 100% | 14.72% | 06-Aug-26 | 13-Sep-26 | 18-Jul-26 A | 04-Nov-26 | 79,923.17 | 11,767.40 | 79,923.17 | -44 |
| MLTX-02-005-CN-1 | Installing UPVC Pipes for External Connection for Sewage | 4 | 100% | 0% | 15-Aug-26 | 18-Aug-26 | 05-Oct-26 | 08-Oct-26 | 14,217.67 | 0.00 | 14,217.67 | -43 |
| MLTX-02-005-CN-1 | Installing UPVC Pipes for Sewage Network | 2 | 100% | 100% | 06-Aug-26 | 08-Aug-26 | 18-Jul-26 A | 22-Jul-26 A | 11,767.40 | 11,767.40 | 11,767.40 | 14 |
| MLTX-02-005-CN-1 | Installing of Plumping Fixtures and Accessories | 2 | 100% | 0% | 24-Aug-26 | 25-Aug-26 | 15-Oct-26 | 17-Oct-26 | 10,358.68 | 0.00 | 10,358.68 | -44 |
| MLTX-02-005-CN-1 | Installing Inspection Chamber for Sewage Network | 5 | 100% | 0% | 09-Aug-26 | 13-Aug-26 | 29-Sep-26 | 04-Oct-26 | 12,186.63 | 0.00 | 12,186.63 | -43 |
| MLTX-02-005-CN-1 | Installing of Toilet Fixtures and Accessories Such as Closets | 4 | 100% | 0% | 09-Sep-26 | 13-Sep-26 | 01-Nov-26 | 04-Nov-26 | 31,392.79 | 0.00 | 31,392.79 | -44 |
| **FIRE PROTECTION** | | 2 | 100% | 0% | 20-Sep-26 | 21-Sep-26 | 11-Nov-26 | 12-Nov-26 | 1,949.87 | 0.00 | 1,949.87 | -44 |
| MLTX-02-005-CN-1 | Installing of Fire Fighting Extinguisher and accessories | 2 | 100% | 0% | 20-Sep-26 | 21-Sep-26 | 11-Nov-26 | 12-Nov-26 | 1,949.87 | 0.00 | 1,949.87 | -44 |
| **ELECTRICAL WORKS** | | 113 | 100% | 53.29% | 28-Jul-26 | 26-Sep-26 | 19-Jul-26 A | 30-Nov-26 | 386,998.59 | 206,217.32 | 386,998.59 | -56 |
| **ROUGH-IN WORKS** | | 82 | 100% | 100% | 28-Jul-26 | 05-Aug-26 | 19-Jul-26 A | 09-Aug-26 A | 206,217.32 | 206,217.32 | 206,217.32 | -2 |
| MLTX-02-005-CN-1 | Preleminary Works for Earthing Works | 2 | 100% | 100% | 28-Jul-26 | 29-Jul-26 | 19-Jul-26 A | 09-Aug-26 A | 32,172.69 | 32,172.69 | 32,172.69 | -8 |
| MLTX-02-005-CN-1 | Preleminary Works for Panel Boards | 2 | 100% | 100% | 28-Jul-26 | 29-Jul-26 | 19-Jul-26 A | 20-Jul-26 A | 68,245.12 | 68,245.12 | 68,245.12 | 8 |
| MLTX-02-005-CN-1 | Preleminary Works for Cable Works | 2 | 100% | 100% | 04-Aug-26 | 05-Aug-26 | 19-Jul-26 A | 22-Jul-26 A | 12,488.92 | 12,488.92 | 12,488.92 | 12 |
| MLTX-02-005-CN-1 | Preleminary Works for Sockets and Power Points | 2 | 100% | 100% | 28-Jul-26 | 29-Jul-26 | 19-Jul-26 A | 20-Jul-26 A | 15,990.55 | 15,990.55 | 15,990.55 | 8 |
| MLTX-02-005-CN-1 | Preleminary Works for Lightning Works | 2 | 100% | 100% | 28-Jul-26 | 29-Jul-26 | 19-Jul-26 A | 09-Aug-26 A | 21,935.93 | 21,935.93 | 21,935.93 | -8 |
| MLTX-02-005-CN-1 | Preleminary Works for Data & Telecommunication System | 2 | 100% | 100% | 28-Jul-26 | 29-Jul-26 | 19-Jul-26 A | 09-Aug-26 A | 24,470.75 | 24,470.75 | 24,470.75 | -8 |
| MLTX-02-005-CN-1 | Preleminary Works for Security and Access Control System | 2 | 100% | 100% | 28-Jul-26 | 29-Jul-26 | 19-Jul-26 A | 09-Aug-26 A | 30,913.36 | 30,913.36 | 30,913.36 | -8 |
| **FIXTURE WORKS** | | 19 | 100% | 0% | 17-Sep-26 | 26-Sep-26 | 09-Nov-26 | 30-Nov-26 | 180,781.27 | 0.00 | 180,781.27 | -56 |
| MLTX-02-005-CN-1 | Installing and Finish Works of Panel Boards | 5 | 100% | 0% | 17-Sep-26 | 22-Sep-26 | 09-Nov-26 | 14-Nov-26 | 102,367.69 | 0.00 | 102,367.69 | -44 |
| MLTX-02-005-CN-1 | Installing Data and Telecommunication System with all | 4 | 100% | 0% | 20-Sep-26 | 24-Sep-26 | 11-Nov-26 | 15-Nov-26 | 6,239.59 | 0.00 | 6,239.59 | -44 |
| MLTX-02-005-CN-1 | Installing and Finalize Works of Sockets and Power Points | 4 | 100% | 0% | 20-Sep-26 | 24-Sep-26 | 11-Nov-26 | 15-Nov-26 | 7,085.10 | 0.00 | 7,085.10 | -44 |
| MLTX-02-005-CN-1 | Installing and Finalize Works of Earthing Works | 3 | 100% | 0% | 17-Sep-26 | 20-Sep-26 | 09-Nov-26 | 11-Nov-26 | 6,824.51 | 0.00 | 6,824.51 | -44 |
| MLTX-02-005-CN-1 | Installing of Fire automation and Fire Alarm System | 4 | 100% | 0% | 21-Sep-26 | 26-Sep-26 | 12-Nov-26 | 16-Nov-26 | 34,317.53 | 0.00 | 34,317.53 | -44 |
| MLTX-02-005-CN-1 | Installing and Finalize Works of Lighting Works including Light | 4 | 100% | 0% | 20-Sep-26 | 24-Sep-26 | 11-Nov-26 | 15-Nov-26 | 14,259.43 | 0.00 | 14,259.43 | -44 |

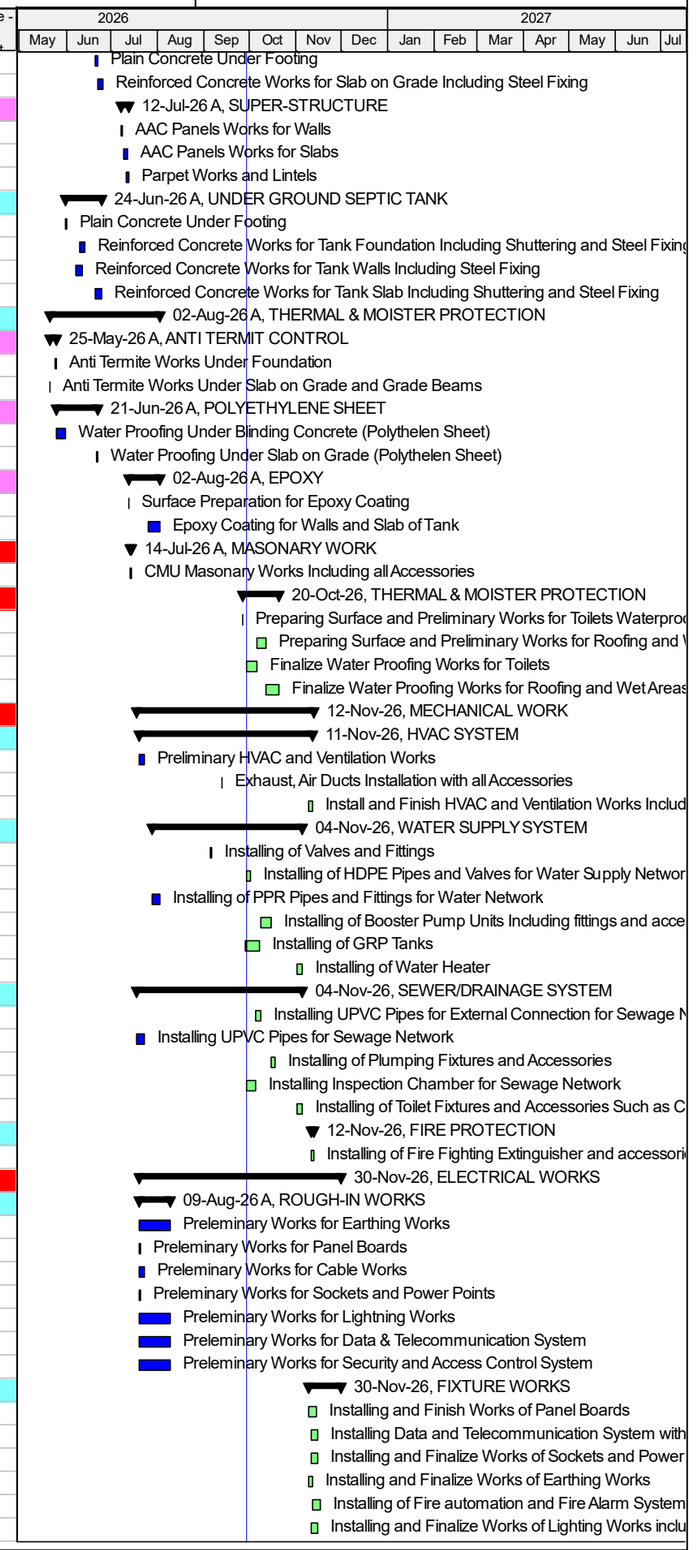


Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary




TASK filter: All Activities

© Oracle Corporation

# MLTX-02-005 - Playground Initiative for Eastern Region (Arar-Hasa osis -Dammam)

**Updateded schedule**
**D.D 28-09-2026**

| Activity ID | Activity Name | Original Duration | Schedule % Complete | Performance % Complete | BL Project Start | BL Project Finish | Start | Finish | Planned Value Cost | Earned Value Cost | Budgeted Total Cost | Variance - BL Project |
|---|---|---|---|---|---|---|---|---|---|---|---|---|
| MLTX-02-005-CN-1 | Installing and Finalize Works of Lightning Protection System | 6 | 100% | 0% | 17-Sep-26 | 24-Sep-26 | 09-Nov-26 | 15-Nov-26 | 2,437.33 | 0.00 | 2,437.33 | -44 |
| MLTX-02-005-CN-1 | Installing and Finalize Works of Security and Access Control | 4 | 100% | 0% | 17-Sep-26 | 21-Sep-26 | 26-Nov-26 | 30-Nov-26 | 7,250.09 | 0.00 | 7,250.09 | -59 |
| **DOORS/WINDOWS** | | 42 | 100% | 0% | 28-Jul-26 | 26-Sep-26 | 29-Sep-26 | 16-Nov-26 | 68,245.12 | 0.00 | 68,245.12 | -44 |
| MLTX-02-005-CN-111 | Preliminary Works For Windows/Curtain Wall | 2 | 100% | 0% | 28-Jul-26 | 29-Jul-26 | 29-Sep-26 | 30-Sep-26 | 52,646.24 | 0.00 | 52,646.24 | -53 |
| MLTX-02-005-CN-111 | Preliminary Works For Doors | 3 | 100% | 0% | 28-Jul-26 | 30-Jul-26 | 29-Sep-26 | 01-Oct-26 | 7,799.44 | 0.00 | 7,799.44 | -53 |
| MLTX-02-005-CN-111 | Finalize Metal Doors for Toilets Building | 7 | 100% | 0% | 17-Sep-26 | 26-Sep-26 | 09-Nov-26 | 16-Nov-26 | 1,949.86 | 0.00 | 1,949.86 | -44 |
| MLTX-02-005-CN-111 | Finalize Glazzed Curtain Wall Works | 7 | 100% | 0% | 17-Sep-26 | 26-Sep-26 | 09-Nov-26 | 16-Nov-26 | 5,849.58 | 0.00 | 5,849.58 | -44 |
| **METAL WORKS** | | 25 | 100% | 28.57% | 23-Jul-26 | 01-Sep-26 | 16-Sep-26 A | 27-Oct-26 | 13,649.02 | 3,899.72 | 13,649.02 | -47 |
| MLTX-02-005-CN-111 | Installation of Galvanized Steel Ladder | 4 | 100% | 0% | 24-Aug-26 | 27-Aug-26 | 24-Oct-26 | 27-Oct-26 | 5,849.58 | 0.00 | 5,849.58 | -51 |
| MLTX-02-005-CN-111 | Installation of DI Cover for Tank | 4 | 100% | 0% | 23-Jul-26 | 27-Jul-26 | 29-Sep-26 | 03-Oct-26 | 3,899.72 | 0.00 | 3,899.72 | -57 |
| MLTX-02-005-CN-111 | Installation of Galvanized Steel Roof Scupper | 4 | 100% | 100% | 29-Aug-26 | 01-Sep-26 | 16-Sep-26 A | 16-Sep-26 A | 3,899.72 | 3,899.72 | 3,899.72 | -13 |
| **FINISHING WORKS** | | 71 | 100% | 24.42% | 06-Aug-26 | 20-Sep-26 | 10-Aug-26 A | 11-Nov-26 | 166,130.97 | 40,563.60 | 166,130.97 | -44 |
| **FLOOR FINISHES** | | 34 | 100% | 0% | 12-Aug-26 | 20-Sep-26 | 04-Oct-26 | 11-Nov-26 | 17,159.03 | 0.00 | 17,159.03 | -44 |
| MLTX-02-005-CN-1 | Creamic Tiles Floor Finish Works | 2 | 100% | 0% | 12-Aug-26 | 13-Aug-26 | 04-Oct-26 | 05-Oct-26 | 11,894.39 | 0.00 | 11,894.39 | -44 |
| MLTX-02-005-CN-1 | Granite Tiles Floor Finish Works | 4 | 100% | 0% | 15-Aug-26 | 18-Aug-26 | 06-Oct-26 | 10-Oct-26 | 2,924.82 | 0.00 | 2,924.82 | -44 |
| MLTX-02-005-CN-1 | Epoxy Coat on Concrete Floor | 3 | 100% | 0% | 17-Sep-26 | 20-Sep-26 | 09-Nov-26 | 11-Nov-26 | 1,169.94 | 0.00 | 1,169.94 | -44 |
| MLTX-02-005-CN-1 | Ceramic Skirting Tiles Finish Works | 4 | 100% | 0% | 19-Aug-26 | 23-Aug-26 | 11-Oct-26 | 14-Oct-26 | 1,169.88 | 0.00 | 1,169.88 | -44 |
| **WALL FINISHES** | | 70 | 100% | 30.27% | 06-Aug-26 | 19-Sep-26 | 10-Aug-26 A | 10-Nov-26 | 134,001.04 | 40,563.60 | 134,001.04 | -44 |
| MLTX-02-005-CN-1 | Stone Cladding Finish Works for External Walls | 5 | 100% | 0% | 26-Aug-26 | 31-Aug-26 | 11-Oct-26 | 15-Oct-26 | 2,275.00 | 0.00 | 2,275.00 | -38 |
| MLTX-02-005-CN-1 | Glass Partitions including all accessories and doors | 7 | 100% | 0% | 09-Sep-26 | 16-Sep-26 | 01-Nov-26 | 08-Nov-26 | 13,649.02 | 0.00 | 13,649.02 | -44 |
| MLTX-02-005-CN-1 | Granite Capping for Parpet | 2 | 100% | 0% | 22-Aug-26 | 23-Aug-26 | 21-Oct-26 | 22-Oct-26 | 8,150.24 | 0.00 | 8,150.24 | -51 |
| MLTX-02-005-CN-1 | Preliminary Works for Wall Finish Works including Plastering | 5 | 100% | 100% | 06-Aug-26 | 11-Aug-26 | 10-Aug-26 A | 19-Aug-26 A | 18,315.62 | 18,315.62 | 18,315.62 | -7 |
| MLTX-02-005-CN-1 | Preliminary Works for Wall Finish Works (External) | 4 | 100% | 100% | 06-Aug-26 | 10-Aug-26 | 15-Aug-26 A | 29-Aug-26 A | 6,551.63 | 6,551.63 | 6,551.63 | -15 |
| MLTX-02-005-CN-1 | Painting Finish Works for External Walls | 7 | 100% | 0% | 18-Aug-26 | 25-Aug-26 | 03-Oct-26 | 10-Oct-26 | 35,825.58 | 0.00 | 35,825.58 | -38 |
| MLTX-02-005-CN-1 | Ceramic Finish Works for Walls | 5 | 100% | 100% | 15-Aug-26 | 19-Aug-26 | 20-Sep-26 A | 26-Sep-26 A | 15,696.35 | 15,696.35 | 15,696.35 | -31 |
| MLTX-02-005-CN-1 | Phenolic Partitions for Toilets | 7 | 100% | 0% | 01-Sep-26 | 08-Sep-26 | 24-Oct-26 | 31-Oct-26 | 31,197.60 | 0.00 | 31,197.60 | -44 |
| MLTX-02-005-CN-1 | Painting Finish Works for Internal Walls | 2 | 100% | 0% | 17-Sep-26 | 19-Sep-26 | 09-Nov-26 | 10-Nov-26 | 2,340.00 | 0.00 | 2,340.00 | -44 |
| **CELLING FINISHES** | | 10 | 100% | 0% | 12-Aug-26 | 03-Sep-26 | 29-Sep-26 | 10-Oct-26 | 14,970.90 | 0.00 | 14,970.90 | -30 |
| MLTX-02-005-CN-1 | Preliminary Works for Ceiling Painting Works | 3 | 100% | 0% | 12-Aug-26 | 15-Aug-26 | 29-Sep-26 | 01-Oct-26 | 5,771.52 | 0.00 | 5,771.52 | -40 |
| MLTX-02-005-CN-1 | Painting Finish Works for Ceiling | 3 | 100% | 0% | 01-Sep-26 | 03-Sep-26 | 07-Oct-26 | 10-Oct-26 | 3,427.86 | 0.00 | 3,427.86 | -30 |
| MLTX-02-005-CN-1 | Gypsum Board Suspended Ceiling Finish Works For Ceiling | 7 | 100% | 0% | 24-Aug-26 | 31-Aug-26 | 29-Sep-26 | 06-Oct-26 | 5,771.52 | 0.00 | 5,771.52 | -30 |
| **SPECIALTIES WORK** | | 24 | 100% | 0% | 26-Aug-26 | 22-Sep-26 | 18-Oct-26 | 14-Nov-26 | 58,495.83 | 0.00 | 58,495.83 | -44 |
| MLTX-02-005-CN-113 | Installation of Phenolic Locker | 3 | 100% | 0% | 09-Sep-26 | 12-Sep-26 | 01-Nov-26 | 03-Nov-26 | 24,373.26 | 0.00 | 24,373.26 | -44 |
| MLTX-02-005-CN-113 | Sanitary Fixtures and Accessories Works | 5 | 100% | 0% | 26-Aug-26 | 31-Aug-26 | 18-Oct-26 | 22-Oct-26 | 14,623.96 | 0.00 | 14,623.96 | -44 |
| MLTX-02-005-CN-114 | Installation of MODON Logo on the entrance | 3 | 100% | 0% | 20-Sep-26 | 22-Sep-26 | 11-Nov-26 | 14-Nov-26 | 19,498.61 | 0.00 | 19,498.61 | -44 |
| **TESTING & COMMISSIONING** | | 40 | 0% | 0% | 24-Oct-26 | 26-Dec-26 | 17-Feb-27 | 08-Apr-27 | 0.00 | 0.00 | 0.00 | -85 |
| MLTX-02-005-TC-11860 | Testing and Commissioning for MEP Works for Playground | 14 | 0% | 0% | 10-Dec-26 | 26-Dec-26 | 24-Mar-27 | 08-Apr-27 | 0.00 | 0.00 | 0.00 | -85 |
| MLTX-02-005-TC-11870 | Testing and Commissioning for MEP Works for Toilet/Service | 10 | 0% | 0% | 24-Oct-26 | 03-Nov-26 | 17-Feb-27 | 01-Mar-27 | 0.00 | 0.00 | 0.00 | -100 |
| MLTX-02-005-TC-11880 | Testing and Commissioning for MEP Works for Landscape | 11 | 0% | 0% | 24-Oct-26 | 04-Nov-26 | 17-Feb-27 | 02-Mar-27 | 0.00 | 0.00 | 0.00 | -100 |
| **HASA OASIS** | | 246 | 45.43% | 36.64% | 03-Mar-26 | 02-Jan-27 | 04-Mar-26 A | 15-Apr-27 | 4,535,089.67 | 3,657,877.35 | 9,982,829.07 | -85 |
| **MOBILIZATION** | | 24 | 0% | 0% | 03-Mar-26 | 02-Apr-26 | 04-Mar-26 A | 04-Apr-26 A | 0.00 | 0.00 | 0.00 | -1 |
| **TOPOGRAPHIC SURVEY** | | 5 | 0% | 0% | 03-Mar-26 | 08-Mar-26 | 04-Mar-26 A | 08-Mar-26 A | 0.00 | 0.00 | 0.00 | 0 |
| MLTX-02-005-MB-1860 | Site Survey Works | 5 | 100% | 100% | 03-Mar-26 | 08-Mar-26 | 04-Mar-26 A | 08-Mar-26 A | 0.00 | 0.00 | 0.00 | 0 |
| **SITE FACILITIES & OFFICES** | | 23 | 0% | 0% | 03-Mar-26 | 01-Apr-26 | 04-Mar-26 A | 02-Apr-26 A | 0.00 | 0.00 | 0.00 | -1 |
| MLTX-02-005-MB-1740 | Manpower Mobalization | 5 | 100% | 100% | 28-Mar-26 | 01-Apr-26 | 29-Mar-26 A | 02-Apr-26 A | 0.00 | 0.00 | 0.00 | -1 |
| MLTX-02-005-MB-1750 | Equipment Mobalization | 7 | 100% | 100% | 25-Mar-26 | 01-Apr-26 | 26-Mar-26 A | 02-Apr-26 A | 0.00 | 0.00 | 0.00 | -1 |
| MLTX-02-005-MB-1770 | Site Layout Plan | 4 | 100% | 100% | 03-Mar-26 | 07-Mar-26 | 04-Mar-26 A | 08-Mar-26 A | 0.00 | 0.00 | 0.00 | -1 |
| MLTX-02-005-MB-1780 | Clear & Grub for Offices & Access Road | 3 | 100% | 100% | 08-Mar-26 | 10-Mar-26 | 09-Mar-26 A | 11-Mar-26 A | 0.00 | 0.00 | 0.00 | -1 |
| MLTX-02-005-MB-1790 | Construct Site Access Roads | 4 | 100% | 100% | 08-Mar-26 | 11-Mar-26 | 09-Mar-26 A | 12-Mar-26 A | 0.00 | 0.00 | 0.00 | -1 |
| MLTX-02-005-MB-1800 | Construct Temporary Fence | 7 | 100% | 100% | 11-Mar-26 | 18-Mar-26 | 12-Mar-26 A | 19-Mar-26 A | 0.00 | 0.00 | 0.00 | -1 |
| MLTX-02-005-MB-1810 | Construct Site Offices & Storage | 14 | 100% | 100% | 12-Mar-26 | 31-Mar-26 | 14-Mar-26 A | 01-Apr-26 A | 0.00 | 0.00 | 0.00 | -1 |
| MLTX-02-005-MB-1820 | Install Project Signs | 8 | 100% | 100% | 12-Mar-26 | 24-Mar-26 | 14-Mar-26 A | 25-Mar-26 A | 0.00 | 0.00 | 0.00 | -1 |
| MLTX-02-005-MB-1830 | Install Site Facilities | 4 | 100% | 100% | 19-Mar-26 | 26-Mar-26 | 24-Mar-26 A | 28-Mar-26 A | 0.00 | 0.00 | 0.00 | -1 |
| MLTX-02-005-MB-1840 | Electrical Works & Connections | 6 | 100% | 100% | 19-Mar-26 | 29-Mar-26 | 24-Mar-26 A | 30-Mar-26 A | 0.00 | 0.00 | 0.00 | -1 |
| MLTX-02-005-MB-1850 | Construct Parking Sheds | 6 | 100% | 100% | 19-Mar-26 | 29-Mar-26 | 24-Mar-26 A | 30-Mar-26 A | 0.00 | 0.00 | 0.00 | -1 |
| **PRELIMINARY SUBMITTALS** | | 20 | 0% | 0% | 08-Mar-26 | 02-Apr-26 | 09-Mar-26 A | 04-Apr-26 A | 0.00 | 0.00 | 0.00 | -1 |
| **PREPARATIONS & SUBMITTAL BY CONTRACTORS** | | 10 | 0% | 0% | 08-Mar-26 | 18-Mar-26 | 09-Mar-26 A | 19-Mar-26 A | 0.00 | 0.00 | 0.00 | -1 |
| MLTX-02-005-MB-176 | Preparation and Submittal of Detailed Work Order | 10 | 100% | 100% | 08-Mar-26 | 18-Mar-26 | 09-Mar-26 A | 19-Mar-26 A | 0.00 | 0.00 | 0.00 | -1 |
| MLTX-02-005-MB-187 | Preparation and Submittal of Project Execution Plan | 8 | 100% | 100% | 08-Mar-26 | 16-Mar-26 | 09-Mar-26 A | 17-Mar-26 A | 0.00 | 0.00 | 0.00 | -1 |
| MLTX-02-005-MB-188 | Submission of Contractor Project Quality Plan | 8 | 100% | 100% | 08-Mar-26 | 16-Mar-26 | 09-Mar-26 A | 17-Mar-26 A | 0.00 | 0.00 | 0.00 | -1 |
| MLTX-02-005-MB-189 | Submission of Construction Safety & Environmental | 8 | 100% | 100% | 08-Mar-26 | 16-Mar-26 | 09-Mar-26 A | 17-Mar-26 A | 0.00 | 0.00 | 0.00 | -1 |
| MLTX-02-005-MB-190 | Preparation and Submittal of Organization Chart | 8 | 100% | 100% | 08-Mar-26 | 16-Mar-26 | 09-Mar-26 A | 17-Mar-26 A | 0.00 | 0.00 | 0.00 | -1 |
| MLTX-02-005-MB-191 | Preparation and Submittal of Communication Plan | 8 | 100% | 100% | 08-Mar-26 | 16-Mar-26 | 09-Mar-26 A | 17-Mar-26 A | 0.00 | 0.00 | 0.00 | -1 |
| **APPROVALS BY EMPLOYERS** | | 12 | 0% | 0% | 17-Mar-26 | 02-Apr-26 | 18-Mar-26 A | 04-Apr-26 A | 0.00 | 0.00 | 0.00 | -1 |

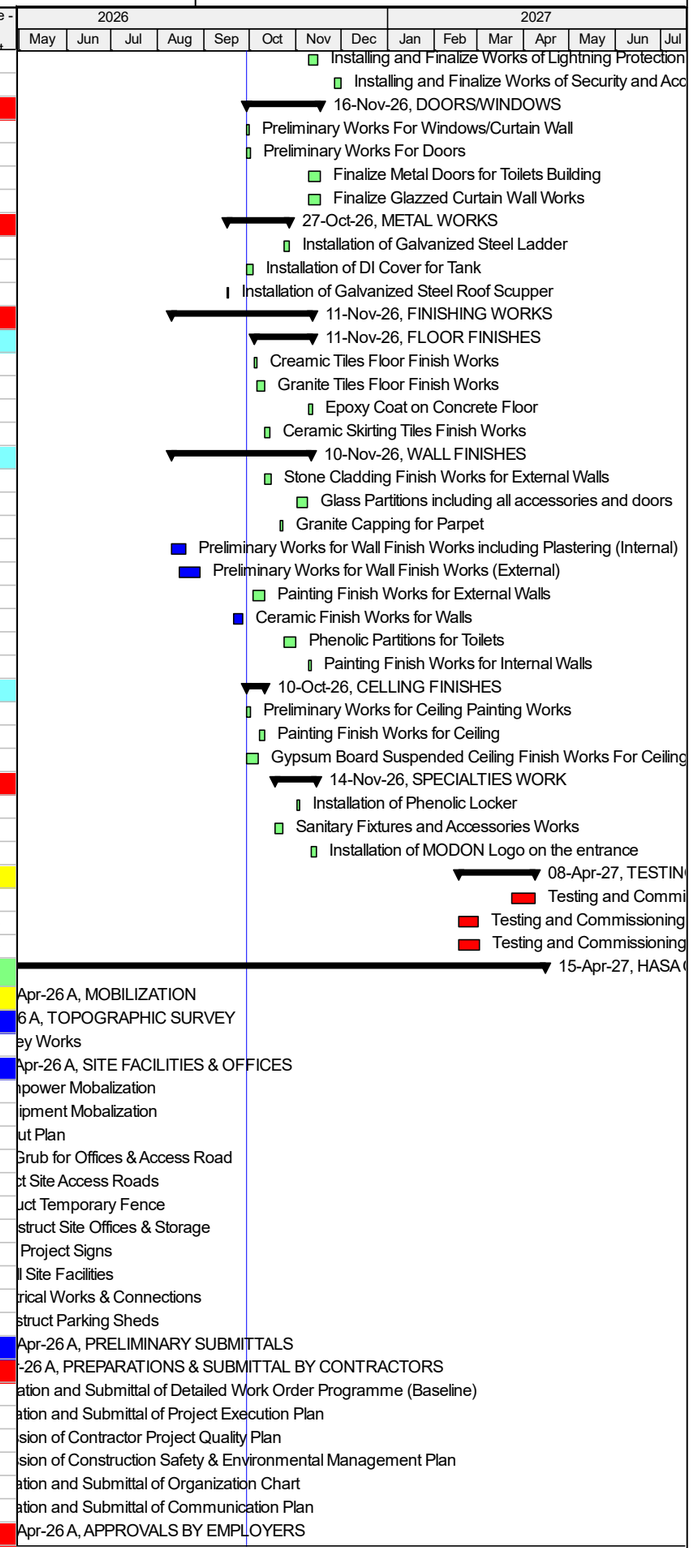




© Oracle Corporation

# MLTX-02-005 - Playground Initiative for Eastern Region (Arar-Hasa osis -Dammam)


**Updateded schedule**
**D.D 28-09-2026**

PROFAST شركة برو فاست المحدودة

egis

MODON

| Activity ID | Activity Name | Original Duration | Schedule % Complete | Performance % Complete | BL Project Start | BL Project Finish | Start | Finish | Planned Value Cost | Earned Value Cost | Budgeted Total Cost | Variance - BL Project |
|---|---|---|---|---|---|---|---|---|---|---|---|---|
| MLTX-02-005-MB-192 | Approval of Detailed Work Order Programme (Baseline) | 10 | 100% | 100% | 19-Mar-26 | 02-Apr-26 | 24-Mar-26 A | 04-Apr-26 A | 0.00 | 0.00 | 0.00 | -1 |
| MLTX-02-005-MB-193 | Approval of Project Execution Plan | 10 | 100% | 100% | 17-Mar-26 | 31-Mar-26 | 18-Mar-26 A | 01-Apr-26 A | 0.00 | 0.00 | 0.00 | -1 |
| MLTX-02-005-MB-194 | Approval of Contractor Project Quality Plan | 10 | 100% | 100% | 17-Mar-26 | 31-Mar-26 | 18-Mar-26 A | 01-Apr-26 A | 0.00 | 0.00 | 0.00 | -1 |
| MLTX-02-005-MB-195 | Approval of Construction Safety & Environmental | 10 | 100% | 100% | 17-Mar-26 | 31-Mar-26 | 18-Mar-26 A | 01-Apr-26 A | 0.00 | 0.00 | 0.00 | -1 |
| MLTX-02-005-MB-196 | Approval of Organization Chart | 10 | 100% | 100% | 17-Mar-26 | 31-Mar-26 | 18-Mar-26 A | 01-Apr-26 A | 0.00 | 0.00 | 0.00 | -1 |
| MLTX-02-005-MB-197 | Approval of Communication Plan | 10 | 100% | 100% | 17-Mar-26 | 31-Mar-26 | 18-Mar-26 A | 01-Apr-26 A | 0.00 | 0.00 | 0.00 | -1 |
| **ENGINEERING** | | 121 | 0% | 0% | 08-Mar-26 | 20-Sep-26 | 08-Mar-26 A | 16-Nov-26 | 0.00 | 0.00 | 0.00 | -48 |
| **SHOP DRAWINGS** | | 120 | 0% | 0% | 09-Mar-26 | 20-Sep-26 | 09-Mar-26 A | 16-Nov-26 | 0.00 | 0.00 | 0.00 | -48 |
| **SHOP DRAWINGS SUBMISSION** | | 104 | 0% | 0% | 09-Mar-26 | 06-Sep-26 | 09-Mar-26 A | 02-Nov-26 | 0.00 | 0.00 | 0.00 | -48 |
| **SHOP DRAWING SUBMITTALS FOR EARTHING WORKS** | | 15 | 0% | 0% | 09-Mar-26 | 29-Mar-26 | 09-Mar-26 A | 14-Mar-26 A | 0.00 | 0.00 | 0.00 | 10 |
| MLTX-02-005-EN-7 | Shop DWG Submittal for Layout Plan | 15 | 100% | 100% | 09-Mar-26 | 29-Mar-26 | 09-Mar-26 A | 14-Mar-26 A | 0.00 | 0.00 | 0.00 | 10 |
| MLTX-02-005-EN-7 | Shop DWG Submittal for Setting Out | 15 | 100% | 100% | 09-Mar-26 | 29-Mar-26 | 09-Mar-26 A | 14-Mar-26 A | 0.00 | 0.00 | 0.00 | 10 |
| MLTX-02-005-EN-7 | Shop DWG Submittal for Grading Layout Plan | 15 | 100% | 100% | 09-Mar-26 | 29-Mar-26 | 09-Mar-26 A | 14-Mar-26 A | 0.00 | 0.00 | 0.00 | 10 |
| MLTX-02-005-EN-7 | Shop DWG Submittal for Curb Setting Out Points | 15 | 100% | 100% | 09-Mar-26 | 29-Mar-26 | 09-Mar-26 A | 14-Mar-26 A | 0.00 | 0.00 | 0.00 | 10 |
| MLTX-02-005-EN-7 | Shop DWG Submittal for Signing & Marking Layout Plan | 15 | 100% | 100% | 09-Mar-26 | 29-Mar-26 | 09-Mar-26 A | 14-Mar-26 A | 0.00 | 0.00 | 0.00 | 10 |
| MLTX-02-005-EN-7 | Shop DWG Submittal for Standards Details | 15 | 100% | 100% | 09-Mar-26 | 29-Mar-26 | 09-Mar-26 A | 14-Mar-26 A | 0.00 | 0.00 | 0.00 | 10 |
| **SHOP DRAWING SUBMITTALS FOR SERVICE/TOILET WORKS** | | 42 | 0% | 0% | 09-Mar-26 | 22-Apr-26 | 09-Mar-26 A | 30-Jul-26 A | 0.00 | 0.00 | 0.00 | -82 |
| **ARCHITECTURE WORKS** | | 15 | 0% | 0% | 09-Mar-26 | 29-Mar-26 | 09-Mar-26 A | 14-Mar-26 A | 0.00 | 0.00 | 0.00 | 10 |
| MLTX-02-005-EN | Shop DWG Submittal for Floor Plan | 15 | 100% | 100% | 09-Mar-26 | 29-Mar-26 | 09-Mar-26 A | 14-Mar-26 A | 0.00 | 0.00 | 0.00 | 10 |
| MLTX-02-005-EN | Shop DWG Submittal for Elevations | 15 | 100% | 100% | 09-Mar-26 | 29-Mar-26 | 09-Mar-26 A | 14-Mar-26 A | 0.00 | 0.00 | 0.00 | 10 |
| MLTX-02-005-EN | Shop DWG Submittal for Sections | 15 | 100% | 100% | 09-Mar-26 | 29-Mar-26 | 09-Mar-26 A | 14-Mar-26 A | 0.00 | 0.00 | 0.00 | 10 |
| MLTX-02-005-EN | Shop DWG Submittal for Ceiling Plan | 15 | 100% | 100% | 09-Mar-26 | 29-Mar-26 | 09-Mar-26 A | 14-Mar-26 A | 0.00 | 0.00 | 0.00 | 10 |
| MLTX-02-005-EN | Shop DWG Submittal for Finishes Plan | 15 | 100% | 100% | 09-Mar-26 | 29-Mar-26 | 09-Mar-26 A | 14-Mar-26 A | 0.00 | 0.00 | 0.00 | 10 |
| MLTX-02-005-EN | Shop DWG Submittal for Toilet Details | 15 | 100% | 100% | 09-Mar-26 | 29-Mar-26 | 09-Mar-26 A | 14-Mar-26 A | 0.00 | 0.00 | 0.00 | 10 |
| MLTX-02-005-EN | Shop DWG Submittal for Doors/Windows Schedule | 15 | 100% | 100% | 09-Mar-26 | 29-Mar-26 | 09-Mar-26 A | 14-Mar-26 A | 0.00 | 0.00 | 0.00 | 10 |
| **STRUCTURE WORKS** | | 21 | 0% | 0% | 30-Mar-26 | 22-Apr-26 | 15-Mar-26 A | 19-Mar-26 A | 0.00 | 0.00 | 0.00 | 26 |
| MLTX-02-005-EN | Shop DWG Submittal for Foundation Plan | 15 | 100% | 100% | 30-Mar-26 | 15-Apr-26 | 15-Mar-26 A | 19-Mar-26 A | 0.00 | 0.00 | 0.00 | 20 |
| MLTX-02-005-EN | Shop DWG Submittal for Ground Floor Framing Plan | 21 | 100% | 100% | 30-Mar-26 | 22-Apr-26 | 15-Mar-26 A | 19-Mar-26 A | 0.00 | 0.00 | 0.00 | 26 |
| MLTX-02-005-EN | Shop DWG Submittal for Sections/Details | 21 | 100% | 100% | 30-Mar-26 | 22-Apr-26 | 15-Mar-26 A | 19-Mar-26 A | 0.00 | 0.00 | 0.00 | 26 |
| **MECHANCAL WORKS** | | 27 | 0% | 0% | 30-Mar-26 | 22-Apr-26 | 15-Mar-26 A | 07-Jul-26 A | 0.00 | 0.00 | 0.00 | -62 |
| MLTX-02-005-EN | Shop DWG Submittal for HVAC Plan | 21 | 100% | 100% | 30-Mar-26 | 22-Apr-26 | 15-Mar-26 A | 19-Mar-26 A | 0.00 | 0.00 | 0.00 | 26 |
| MLTX-02-005-EN | Shop DWG Submittal for Exhaust Air Plan | 21 | 100% | 100% | 30-Mar-26 | 22-Apr-26 | 15-Mar-26 A | 19-Mar-26 A | 0.00 | 0.00 | 0.00 | 26 |
| MLTX-02-005-EN | Shop DWG Submittal for HVAC Equipment Schedule | 21 | 100% | 100% | 30-Mar-26 | 22-Apr-26 | 15-Mar-26 A | 19-Mar-26 A | 0.00 | 0.00 | 0.00 | 26 |
| MLTX-02-005-EN | Shop DWG Submittal for Fire Fighting Layout | 21 | 100% | 100% | 30-Mar-26 | 22-Apr-26 | 15-Mar-26 A | 19-Mar-26 A | 0.00 | 0.00 | 0.00 | 26 |
| MLTX-02-005-EN | Shop DWG Submittal for Water Supply Layout | 21 | 100% | 100% | 30-Mar-26 | 22-Apr-26 | 15-Mar-26 A | 20-May-26 A | 0.00 | 0.00 | 0.00 | -24 |
| MLTX-02-005-EN | Shop DWG Submittal for Water Supply Details | 21 | 100% | 100% | 30-Mar-26 | 22-Apr-26 | 15-Mar-26 A | 20-May-26 A | 0.00 | 0.00 | 0.00 | -24 |
| MLTX-02-005-EN | Shop DWG Submittal for Drainage Layout | 21 | 100% | 100% | 30-Mar-26 | 22-Apr-26 | 15-Mar-26 A | 02-Jun-26 A | 0.00 | 0.00 | 0.00 | -32 |
| MLTX-02-005-EN | Shop DWG Submittal for Drainage Details | 21 | 100% | 100% | 30-Mar-26 | 22-Apr-26 | 15-Mar-26 A | 02-Jun-26 A | 0.00 | 0.00 | 0.00 | -32 |
| MLTX-02-005-EN | Shop DWG Submittal for Dut Routing Layout | 21 | 100% | 100% | 30-Mar-26 | 22-Apr-26 | 15-Mar-26 A | 19-Mar-26 A | 0.00 | 0.00 | 0.00 | 26 |
| MLTX-02-005-EN | Shop DWG Submittal for Diffusers Layout | 21 | 100% | 100% | 30-Mar-26 | 22-Apr-26 | 07-Jul-26 A | 07-Jul-26 A | 0.00 | 0.00 | 0.00 | -62 |
| **ELECTRICAL WORKS** | | 27 | 0% | 0% | 30-Mar-26 | 22-Apr-26 | 15-Mar-26 A | 30-Jul-26 A | 0.00 | 0.00 | 0.00 | -82 |
| MLTX-02-005-EN | Shop DWG Submittal for Lighting Layout | 21 | 100% | 100% | 30-Mar-26 | 22-Apr-26 | 15-Mar-26 A | 19-Mar-26 A | 0.00 | 0.00 | 0.00 | 26 |
| MLTX-02-005-EN | Shop DWG Submittal for Power Layout | 21 | 100% | 100% | 30-Mar-26 | 22-Apr-26 | 15-Mar-26 A | 19-Mar-26 A | 0.00 | 0.00 | 0.00 | 26 |
| MLTX-02-005-EN | Shop DWG Submittal for Power Single Line Diagram | 21 | 100% | 100% | 30-Mar-26 | 22-Apr-26 | 10-Jun-26 A | 10-Jun-26 A | 0.00 | 0.00 | 0.00 | -39 |
| MLTX-02-005-EN | Shop DWG Submittal for Panel Board Schedules | 15 | 100% | 100% | 30-Mar-26 | 15-Apr-26 | 10-Jun-26 A | 10-Jun-26 A | 0.00 | 0.00 | 0.00 | -45 |
| MLTX-02-005-EN | Shop DWG Submittal for Lighting Installation Details | 21 | 100% | 100% | 30-Mar-26 | 22-Apr-26 | 15-Mar-26 A | 19-Mar-26 A | 0.00 | 0.00 | 0.00 | 26 |
| MLTX-02-005-EN | Shop DWG Submittal for Power Installation Details | 15 | 100% | 100% | 30-Mar-26 | 15-Apr-26 | 15-Mar-26 A | 19-Mar-26 A | 0.00 | 0.00 | 0.00 | 20 |
| MLTX-02-005-EN | Shop DWG Submittal for Cable Tray Installation Details | 15 | 100% | 100% | 30-Mar-26 | 15-Apr-26 | 15-Mar-26 A | 19-Mar-26 A | 0.00 | 0.00 | 0.00 | 20 |
| MLTX-02-005-EN | Shop DWG Submittal for Manhole & Ductbank Details | 15 | 100% | 100% | 30-Mar-26 | 15-Apr-26 | 15-Mar-26 A | 19-Mar-26 A | 0.00 | 0.00 | 0.00 | 20 |
| MLTX-02-005-EN | Shop DWG Submittal for Grounding Details | 15 | 100% | 100% | 30-Mar-26 | 15-Apr-26 | 15-Mar-26 A | 19-Mar-26 A | 0.00 | 0.00 | 0.00 | 20 |
| MLTX-02-005-EN | Shop DWG Submittal for Lightning Protection Details | 15 | 100% | 100% | 30-Mar-26 | 15-Apr-26 | 15-Mar-26 A | 19-Mar-26 A | 0.00 | 0.00 | 0.00 | 20 |
| MLTX-02-005-EN | Shop DWG Submittal for Fire Alarm Installation Details | 15 | 100% | 100% | 30-Mar-26 | 15-Apr-26 | 15-Mar-26 A | 19-Mar-26 A | 0.00 | 0.00 | 0.00 | 20 |
| MLTX-02-005-EN | Shop DWG Submittal for CCTV Details | 15 | 100% | 100% | 30-Mar-26 | 15-Apr-26 | 30-Jul-26 A | 30-Jul-26 A | 0.00 | 0.00 | 0.00 | -88 |
| MLTX-02-005-EN | Shop DWG Submittal for Grounding Layout | 15 | 100% | 100% | 30-Mar-26 | 15-Apr-26 | 15-Mar-26 A | 19-Mar-26 A | 0.00 | 0.00 | 0.00 | 20 |
| MLTX-02-005-EN | Shop DWG Submittal for Lightning Protection System Layout | 15 | 100% | 100% | 30-Mar-26 | 15-Apr-26 | 15-Mar-26 A | 19-Mar-26 A | 0.00 | 0.00 | 0.00 | 20 |
| MLTX-02-005-EN | Shop DWG Submittal for Fire Alarm Layout | 15 | 100% | 100% | 30-Mar-26 | 15-Apr-26 | 15-Mar-26 A | 19-Mar-26 A | 0.00 | 0.00 | 0.00 | 20 |
| MLTX-02-005-EN | Shop DWG Submittal for Fire Alarm Riser Diagram | 15 | 100% | 100% | 30-Mar-26 | 15-Apr-26 | 15-Mar-26 A | 19-Mar-26 A | 0.00 | 0.00 | 0.00 | 20 |
| MLTX-02-005-EN | Shop DWG Submittal for CCTV Layout | 15 | 100% | 100% | 30-Mar-26 | 15-Apr-26 | 15-Mar-26 A | 19-Mar-26 A | 0.00 | 0.00 | 0.00 | 20 |
| MLTX-02-005-EN | Shop DWG Submittal for CCTV Riser Diagram | 15 | 100% | 100% | 30-Mar-26 | 15-Apr-26 | 15-Mar-26 A | 19-Mar-26 A | 0.00 | 0.00 | 0.00 | 20 |
| MLTX-02-005-EN | Shop DWG Submittal for Telephone & Data Layout | 21 | 100% | 100% | 30-Mar-26 | 22-Apr-26 | 15-Mar-26 A | 19-Mar-26 A | 0.00 | 0.00 | 0.00 | 26 |
| MLTX-02-005-EN | Shop DWG Submittal for Telephone & Data Riser Diagram | 21 | 100% | 100% | 30-Mar-26 | 22-Apr-26 | 15-Mar-26 A | 19-Mar-26 A | 0.00 | 0.00 | 0.00 | 26 |
| **SHOP DRAWINGS SUBMITTALS FOR PLAYGROUND WORKS** | | 104 | 0% | 0% | 09-Mar-26 | 06-Sep-26 | 09-Mar-26 A | 02-Nov-26 | 0.00 | 0.00 | 0.00 | -48 |
| **ARCHITECTURE WORKS** | | 41 | 0% | 0% | 09-Mar-26 | 05-Apr-26 | 09-Mar-26 A | 13-Jul-26 A | 0.00 | 0.00 | 0.00 | -82 |
| MLTX-02-005-EN | Shop DWG Submittal for Playground Plan/Layout | 15 | 100% | 100% | 09-Mar-26 | 29-Mar-26 | 09-Mar-26 A | 14-Mar-26 A | 0.00 | 0.00 | 0.00 | 10 |

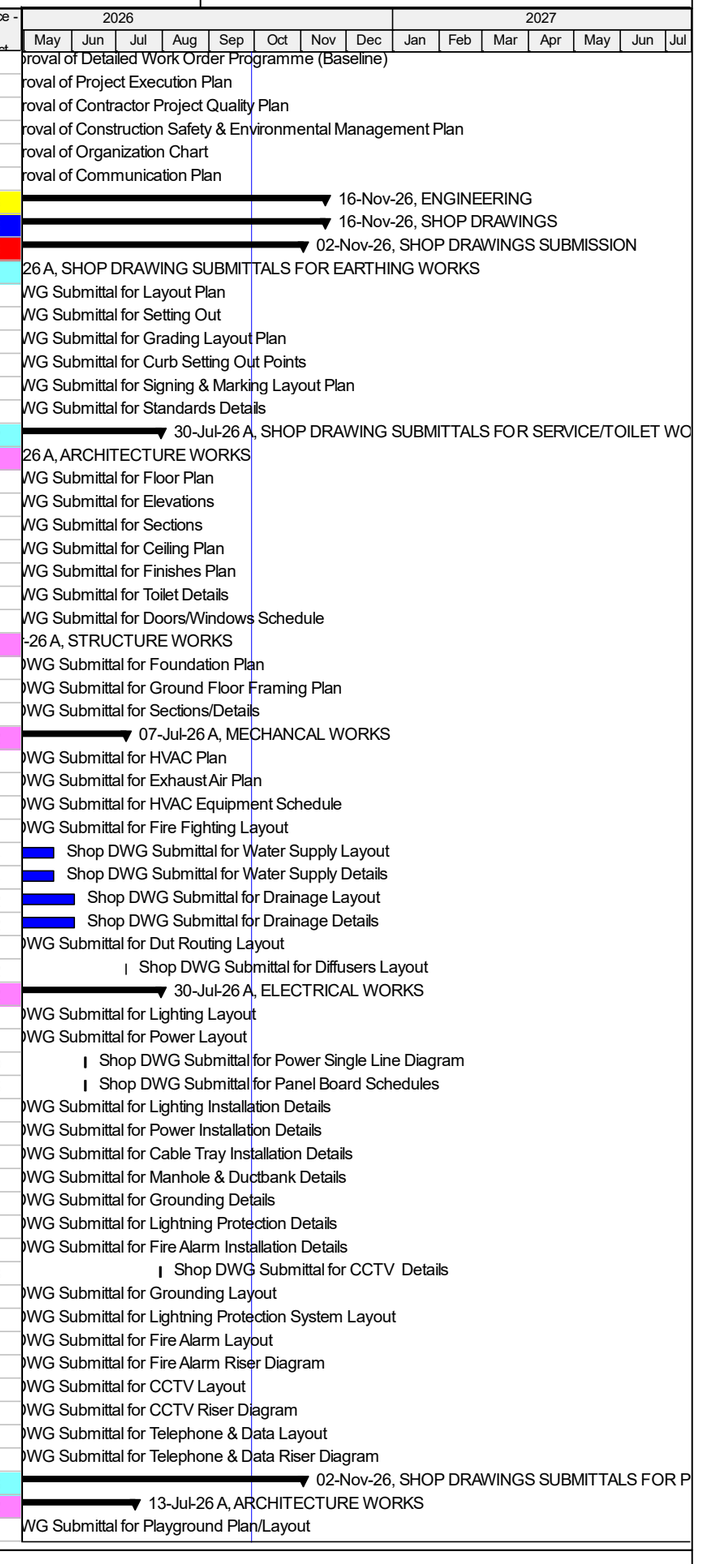


Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary




TASK filter: All Activities

© Oracle Corporation

# MLTX-02-005 - Playground Initiative for Eastern Region (Arar-Hasa osis -Dammam)

**Updateded schedule**
**D.D 28-09-2026**

| Activity ID | Activity Name | Original Duration | Schedule % Complete | Performance % Complete | BL Project Start | BL Project Finish | Start | Finish | Planned Value Cost | Earned Value Cost | Budgeted Total Cost | Variance - BL Project |
|---|---|---|---|---|---|---|---|---|---|---|---|---|
| MLTX-02-005-EN | Shop DWG Submittal for Furniture & Marking | 15 | 100% | 100% | 09-Mar-26 | 29-Mar-26 | 09-Mar-26 A | 28-Apr-26 A | 0.00 | 0.00 | 0.00 | -26 |
| MLTX-02-005-EN | Shop DWG Submittal for Sections | 15 | 100% | 100% | 09-Mar-26 | 29-Mar-26 | 09-Mar-26 A | 14-Mar-26 A | 0.00 | 0.00 | 0.00 | 10 |
| MLTX-02-005-EN | Shop DWG Submittal for Interlock Pattern Plan | 21 | 100% | 100% | 09-Mar-26 | 05-Apr-26 | 09-Mar-26 A | 14-Mar-26 A | 0.00 | 0.00 | 0.00 | 16 |
| MLTX-02-005-EN | Shop DWG Submittal for Doors/Windows Schedule | 21 | 100% | 100% | 09-Mar-26 | 05-Apr-26 | 13-Jul-26 A | 13-Jul-26 A | 0.00 | 0.00 | 0.00 | -82 |
| MLTX-02-005-EN | Shop DWG Submittal for Dome Internal Layout | 21 | 100% | 100% | 09-Mar-26 | 05-Apr-26 | 09-Mar-26 A | 20-May-26 A | 0.00 | 0.00 | 0.00 | -39 |
| **STRUCTURE WORKS** | | 35 | 0% | 0% | 06-Apr-26 | 29-Apr-26 | 15-Mar-26 A | 14-Jul-26 A | 0.00 | 0.00 | 0.00 | -62 |
| MLTX-02-005-EN | Shop DWG Submittal for Air Dome System | 21 | 100% | 100% | 06-Apr-26 | 29-Apr-26 | 15-Mar-26 A | 10-May-26 A | 0.00 | 0.00 | 0.00 | -9 |
| MLTX-02-005-EN | Shop DWG Submittal for Foundation of Air Dome | 21 | 100% | 100% | 06-Apr-26 | 29-Apr-26 | 14-Jul-26 A | 14-Jul-26 A | 0.00 | 0.00 | 0.00 | -62 |
| MLTX-02-005-EN | Shop DWG Submittal for Anchor Bolt Layout of Air Dome | 21 | 100% | 100% | 06-Apr-26 | 29-Apr-26 | 14-Jul-26 A | 14-Jul-26 A | 0.00 | 0.00 | 0.00 | -62 |
| **AIR DOME SYSTEM** | | 21 | 0% | 0% | 06-Apr-26 | 29-Apr-26 | 15-Mar-26 A | 25-May-26 A | 0.00 | 0.00 | 0.00 | -22 |
| MLTX-02-005-EN | Shop DWG Submittal for Air Dome Structural Layout | 21 | 100% | 100% | 06-Apr-26 | 29-Apr-26 | 15-Mar-26 A | 10-May-26 A | 0.00 | 0.00 | 0.00 | -9 |
| MLTX-02-005-EN | Shop DWG Submittal for Membrane Panel Layout | 21 | 100% | 100% | 06-Apr-26 | 29-Apr-26 | 15-Mar-26 A | 25-May-26 A | 0.00 | 0.00 | 0.00 | -22 |
| MLTX-02-005-EN | Shop DWG Submittal for Cable Tension Layout | 21 | 100% | 100% | 06-Apr-26 | 29-Apr-26 | 15-Mar-26 A | 25-May-26 A | 0.00 | 0.00 | 0.00 | -22 |
| MLTX-02-005-EN | Shop DWG Submittal for Airlock Door Details | 21 | 100% | 100% | 06-Apr-26 | 29-Apr-26 | 15-Mar-26 A | 25-May-26 A | 0.00 | 0.00 | 0.00 | -22 |
| MLTX-02-005-EN | Shop DWG Submittal for Emergency Exit Details | 21 | 100% | 100% | 06-Apr-26 | 29-Apr-26 | 15-Mar-26 A | 25-May-26 A | 0.00 | 0.00 | 0.00 | -22 |
| **SPORTS EQUIPMENT** | | 21 | 0% | 0% | 06-Apr-26 | 29-Apr-26 | 29-Jun-26 A | 29-Jun-26 A | 0.00 | 0.00 | 0.00 | -49 |
| MLTX-02-005-EN | Shop DWG Submittal for Football Turf Installation | 21 | 100% | 100% | 06-Apr-26 | 29-Apr-26 | 29-Jun-26 A | 29-Jun-26 A | 0.00 | 0.00 | 0.00 | -49 |
| MLTX-02-005-EN | Shop DWG Submittal for Basketball Court Marking | 21 | 100% | 100% | 06-Apr-26 | 29-Apr-26 | 29-Jun-26 A | 29-Jun-26 A | 0.00 | 0.00 | 0.00 | -49 |
| MLTX-02-005-EN | Shop DWG Submittal for Padel Court Structure | 21 | 100% | 100% | 06-Apr-26 | 29-Apr-26 | 29-Jun-26 A | 29-Jun-26 A | 0.00 | 0.00 | 0.00 | -49 |
| **MECHANCAL WORKS** | | 21 | 0% | 0% | 03-Aug-26 | 26-Aug-26 | 29-Sep-26 | 22-Oct-26 | 0.00 | 0.00 | 0.00 | -48 |
| MLTX-02-005-EN | Shop DWG Submittal for HVAC Plan | 21 | 100% | 0% | 03-Aug-26 | 26-Aug-26 | 29-Sep-26 | 22-Oct-26 | 0.00 | 0.00 | 0.00 | -48 |
| MLTX-02-005-EN | Shop DWG Submittal for Exhaust Air Plan | 21 | 100% | 0% | 03-Aug-26 | 26-Aug-26 | 29-Sep-26 | 22-Oct-26 | 0.00 | 0.00 | 0.00 | -48 |
| **ELECTRICAL WORKS** | | 59 | 0% | 0% | 03-Aug-26 | 06-Sep-26 | 20-Aug-26 A | 02-Nov-26 | 0.00 | 0.00 | 0.00 | -48 |
| MLTX-02-005-EN | Shop DWG Submittal for Lighting Layout | 21 | 100% | 0% | 03-Aug-26 | 26-Aug-26 | 29-Sep-26 | 22-Oct-26 | 0.00 | 0.00 | 0.00 | -48 |
| MLTX-02-005-EN | Shop DWG Submittal for Power Layout | 21 | 100% | 0% | 03-Aug-26 | 26-Aug-26 | 29-Sep-26 | 22-Oct-26 | 0.00 | 0.00 | 0.00 | -48 |
| MLTX-02-005-EN | Shop DWG Submittal for Power Single Line Diagram | 21 | 100% | 0% | 03-Aug-26 | 26-Aug-26 | 29-Sep-26 | 22-Oct-26 | 0.00 | 0.00 | 0.00 | -48 |
| MLTX-02-005-EN | Shop DWG Submittal for Panel Board Schedules | 21 | 100% | 0% | 03-Aug-26 | 26-Aug-26 | 29-Sep-26 | 22-Oct-26 | 0.00 | 0.00 | 0.00 | -48 |
| MLTX-02-005-EN | Shop DWG Submittal for Power Installation Details | 21 | 100% | 0% | 03-Aug-26 | 26-Aug-26 | 29-Sep-26 | 22-Oct-26 | 0.00 | 0.00 | 0.00 | -48 |
| MLTX-02-005-EN | Shop DWG Submittal for Fire Alarm Installation Details | 21 | 100% | 0% | 03-Aug-26 | 26-Aug-26 | 29-Sep-26 | 22-Oct-26 | 0.00 | 0.00 | 0.00 | -48 |
| MLTX-02-005-EN | Shop DWG Submittal for CCTV Details | 21 | 100% | 100% | 03-Aug-26 | 26-Aug-26 | 20-Aug-26 A | 20-Aug-26 A | 0.00 | 0.00 | 0.00 | 5 |
| MLTX-02-005-EN | Shop DWG Submittal for Fire Alarm Layout | 30 | 100% | 0% | 03-Aug-26 | 06-Sep-26 | 29-Sep-26 | 02-Nov-26 | 0.00 | 0.00 | 0.00 | -48 |
| MLTX-02-005-EN | Shop DWG Submittal for Fire Alarm Riser Diagram | 21 | 100% | 0% | 03-Aug-26 | 26-Aug-26 | 29-Sep-26 | 22-Oct-26 | 0.00 | 0.00 | 0.00 | -48 |
| MLTX-02-005-EN | Shop DWG Submittal for CCTV Layout | 21 | 100% | 100% | 03-Aug-26 | 26-Aug-26 | 20-Aug-26 A | 20-Aug-26 A | 0.00 | 0.00 | 0.00 | 5 |
| MLTX-02-005-EN | Shop DWG Submittal for CCTV Riser Diagram | 21 | 100% | 100% | 03-Aug-26 | 26-Aug-26 | 20-Aug-26 A | 20-Aug-26 A | 0.00 | 0.00 | 0.00 | 5 |
| **SHOP DRAWINGS SUBMITTALS FOR LANDSCAPE WORKS** | | 57 | 0% | 0% | 09-Mar-26 | 15-Apr-26 | 09-Mar-26 A | 29-Jul-26 A | 0.00 | 0.00 | 0.00 | -87 |
| **ARCHITECTURE WORKS** | | 30 | 0% | 0% | 09-Mar-26 | 15-Apr-26 | 09-Mar-26 A | 19-Mar-26 A | 0.00 | 0.00 | 0.00 | 20 |
| MLTX-02-005-EN | Shop DWG Submittal for Landscape Layout | 21 | 100% | 100% | 09-Mar-26 | 05-Apr-26 | 09-Mar-26 A | 14-Mar-26 A | 0.00 | 0.00 | 0.00 | 16 |
| MLTX-02-005-EN | Shop DWG Submittal for Hardscape Plan | 21 | 100% | 100% | 09-Mar-26 | 05-Apr-26 | 09-Mar-26 A | 14-Mar-26 A | 0.00 | 0.00 | 0.00 | 16 |
| MLTX-02-005-EN | Shop DWG Submittal for Planting Plan | 15 | 100% | 100% | 30-Mar-26 | 15-Apr-26 | 15-Mar-26 A | 19-Mar-26 A | 0.00 | 0.00 | 0.00 | 20 |
| MLTX-02-005-EN | Shop DWG Submittal for Landscape Details | 15 | 100% | 100% | 09-Mar-26 | 29-Mar-26 | 09-Mar-26 A | 14-Mar-26 A | 0.00 | 0.00 | 0.00 | 10 |
| **MECHANCAL WORKS** | | 30 | 0% | 0% | 09-Mar-26 | 15-Apr-26 | 06-Jul-26 A | 06-Jul-26 A | 0.00 | 0.00 | 0.00 | -67 |
| MLTX-02-005-EN | Shop DWG Submittal for Irrigation Details | 30 | 100% | 100% | 09-Mar-26 | 15-Apr-26 | 06-Jul-26 A | 06-Jul-26 A | 0.00 | 0.00 | 0.00 | -67 |
| MLTX-02-005-EN | Shop DWG Submittal for Irrigation Layout | 30 | 100% | 100% | 09-Mar-26 | 15-Apr-26 | 06-Jul-26 A | 06-Jul-26 A | 0.00 | 0.00 | 0.00 | -67 |
| **ELECTRICAL WORKS** | | 30 | 0% | 0% | 09-Mar-26 | 15-Apr-26 | 29-Jul-26 A | 29-Jul-26 A | 0.00 | 0.00 | 0.00 | -87 |
| MLTX-02-005-EN | Shop DWG Submittal for Lighting General Arrangement | 30 | 100% | 100% | 09-Mar-26 | 15-Apr-26 | 29-Jul-26 A | 29-Jul-26 A | 0.00 | 0.00 | 0.00 | -87 |
| MLTX-02-005-EN | Shop DWG Submittal for Lighting Network Layout | 30 | 100% | 100% | 09-Mar-26 | 15-Apr-26 | 29-Jul-26 A | 29-Jul-26 A | 0.00 | 0.00 | 0.00 | -87 |
| MLTX-02-005-EN | Shop DWG Submittal for Lighting Details | 30 | 100% | 100% | 09-Mar-26 | 15-Apr-26 | 29-Jul-26 A | 29-Jul-26 A | 0.00 | 0.00 | 0.00 | -87 |
| MLTX-02-005-EN | Shop DWG Submittal for Lighting Single Line Diagram | 30 | 100% | 100% | 09-Mar-26 | 15-Apr-26 | 29-Jul-26 A | 29-Jul-26 A | 0.00 | 0.00 | 0.00 | -87 |
| **SHOP DRAWINGS APPROVALS** | | 105 | 0% | 0% | 30-Mar-26 | 20-Sep-26 | 15-Mar-26 A | 16-Nov-26 | 0.00 | 0.00 | 0.00 | -48 |
| **SHOP DRAWING APPROVAL FOR EARTHING WORKS** | | 90 | 0% | 0% | 16-Apr-26 | 02-Aug-26 | 15-Mar-26 A | 29-Mar-26 A | 0.00 | 0.00 | 0.00 | 105 |
| MLTX-02-005-EN-1 | Shop DWG Approval for Layout Plan | 15 | 100% | 100% | 16-Apr-26 | 03-May-26 | 15-Mar-26 A | 29-Mar-26 A | 0.00 | 0.00 | 0.00 | 30 |
| MLTX-02-005-EN-1 | Shop DWG Approval for Setting Out | 15 | 100% | 100% | 04-May-26 | 20-May-26 | 15-Mar-26 A | 29-Mar-26 A | 0.00 | 0.00 | 0.00 | 45 |
| MLTX-02-005-EN-1 | Shop DWG Approval for Grading Layout Plan | 15 | 100% | 100% | 21-May-26 | 10-Jun-26 | 15-Mar-26 A | 29-Mar-26 A | 0.00 | 0.00 | 0.00 | 60 |
| MLTX-02-005-EN-1 | Shop DWG Approval for Curb Setting Out Points | 15 | 100% | 100% | 11-Jun-26 | 28-Jun-26 | 15-Mar-26 A | 29-Mar-26 A | 0.00 | 0.00 | 0.00 | 75 |
| MLTX-02-005-EN-1 | Shop DWG Approval for Signing & Marking Layout Plan | 15 | 100% | 100% | 29-Jun-26 | 15-Jul-26 | 15-Mar-26 A | 29-Mar-26 A | 0.00 | 0.00 | 0.00 | 90 |
| MLTX-02-005-EN-1 | Shop DWG Approval for Standards Details | 15 | 100% | 100% | 16-Jul-26 | 02-Aug-26 | 15-Mar-26 A | 29-Mar-26 A | 0.00 | 0.00 | 0.00 | 105 |
| **SHOP DRAWING APPROVAL FOR SERVICE/TOILET WORKS** | | 63 | 0% | 0% | 30-Mar-26 | 06-Jun-26 | 15-Mar-26 A | 30-Jul-26 A | 0.00 | 0.00 | 0.00 | -47 |
| **ARCHITECTURE WORKS** | | 56 | 0% | 0% | 30-Mar-26 | 06-Jun-26 | 15-Mar-26 A | 29-Mar-26 A | 0.00 | 0.00 | 0.00 | 56 |
| MLTX-02-005-EN | Shop DWG Approval for Floor Plan | 30 | 100% | 100% | 30-Mar-26 | 03-May-26 | 15-Mar-26 A | 29-Mar-26 A | 0.00 | 0.00 | 0.00 | 30 |
| MLTX-02-005-EN | Shop DWG Approval for Elevations | 30 | 100% | 100% | 30-Mar-26 | 03-May-26 | 15-Mar-26 A | 29-Mar-26 A | 0.00 | 0.00 | 0.00 | 30 |
| MLTX-02-005-EN | Shop DWG Approval for Sections | 30 | 100% | 100% | 22-Apr-26 | 30-May-26 | 15-Mar-26 A | 29-Mar-26 A | 0.00 | 0.00 | 0.00 | 50 |
| MLTX-02-005-EN | Shop DWG Approval for Ceiling Plan | 30 | 100% | 100% | 30-Mar-26 | 03-May-26 | 15-Mar-26 A | 29-Mar-26 A | 0.00 | 0.00 | 0.00 | 30 |
| MLTX-02-005-EN | Shop DWG Approval for Finishes Plan | 30 | 100% | 100% | 30-Mar-26 | 03-May-26 | 15-Mar-26 A | 29-Mar-26 A | 0.00 | 0.00 | 0.00 | 30 |
| MLTX-02-005-EN | Shop DWG Approval for Toilet Details | 30 | 100% | 100% | 30-Mar-26 | 03-May-26 | 15-Mar-26 A | 29-Mar-26 A | 0.00 | 0.00 | 0.00 | 30 |

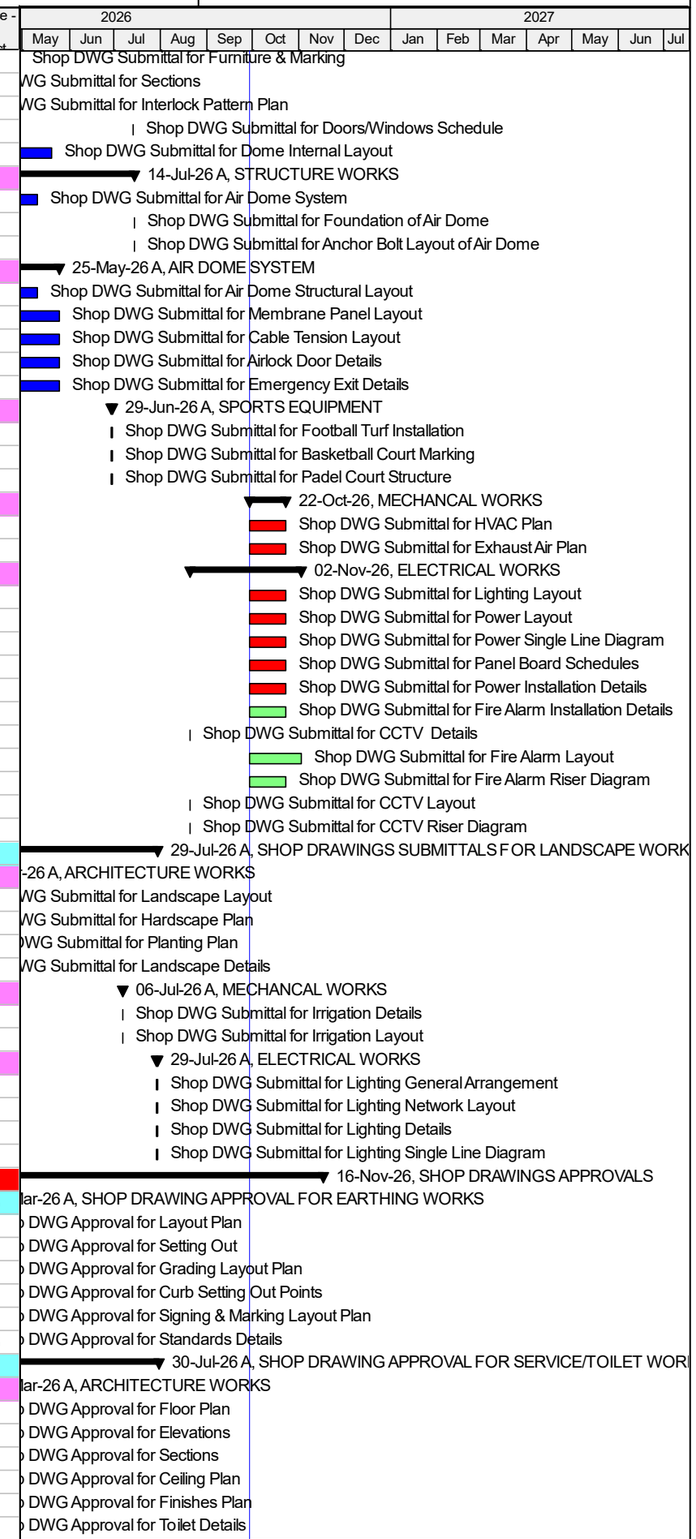


Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary




TASK filter: All Activities

© Oracle Corporation

# MLTX-02-005 - Playground Initiative for Eastern Region (Arar-Hasa osis -Dammam)

**Updateded schedule**
**D.D 28-09-2026**

| Activity ID | Activity Name | Original Duration | Schedule % Complete | Performance % Complete | BL Project Start | BL Project Finish | Start | Finish | Planned Value Cost | Earned Value Cost | Budgeted Total Cost | Variance - BL Project |
|---|---|---|---|---|---|---|---|---|---|---|---|---|
| MLTX-02-005-EN | Shop DWG Approval for Doors/Windows Schedule | 30 | 100% | 100% | 29-Apr-26 | 06-Jun-26 | 15-Mar-26 A | 29-Mar-26 A | 0.00 | 0.00 | 0.00 | 56 |
| **STRUCTURE WORKS** | | 27 | 0% | 0% | 16-Apr-26 | 17-May-26 | 24-Mar-26 A | 04-Apr-26 A | 0.00 | 0.00 | 0.00 | 37 |
| MLTX-02-005-EN | Shop DWG Approval for Foundation Plan | 15 | 100% | 100% | 16-Apr-26 | 03-May-26 | 24-Mar-26 A | 04-Apr-26 A | 0.00 | 0.00 | 0.00 | 25 |
| MLTX-02-005-EN | Shop DWG Approval for Ground Floor Framing Plan | 21 | 100% | 100% | 23-Apr-26 | 17-May-26 | 24-Mar-26 A | 04-Apr-26 A | 0.00 | 0.00 | 0.00 | 37 |
| MLTX-02-005-EN | Shop DWG Approval for Sections/Details | 21 | 100% | 100% | 23-Apr-26 | 17-May-26 | 24-Mar-26 A | 04-Apr-26 A | 0.00 | 0.00 | 0.00 | 37 |
| **MECHANCAL WORKS** | | 36 | 0% | 0% | 23-Apr-26 | 17-May-26 | 24-Mar-26 A | 30-Jul-26 A | 0.00 | 0.00 | 0.00 | -61 |
| MLTX-02-005-EN | Shop DWG Approval for HVAC Plan | 21 | 100% | 100% | 23-Apr-26 | 17-May-26 | 30-Jul-26 A | 30-Jul-26 A | 0.00 | 0.00 | 0.00 | -61 |
| MLTX-02-005-EN | Shop DWG Approval for Exhaust Air Plan | 21 | 100% | 100% | 23-Apr-26 | 17-May-26 | 24-Mar-26 A | 04-Apr-26 A | 0.00 | 0.00 | 0.00 | 37 |
| MLTX-02-005-EN | Shop DWG Approval for HVAC Equipment Schedule | 21 | 100% | 100% | 23-Apr-26 | 17-May-26 | 30-Jul-26 A | 30-Jul-26 A | 0.00 | 0.00 | 0.00 | -61 |
| MLTX-02-005-EN | Shop DWG Approval for Fire Fighting Layout | 21 | 100% | 100% | 23-Apr-26 | 17-May-26 | 24-Mar-26 A | 04-Apr-26 A | 0.00 | 0.00 | 0.00 | 37 |
| MLTX-02-005-EN | Shop DWG Approval for Water Supply Layout | 21 | 100% | 100% | 23-Apr-26 | 17-May-26 | 03-Jun-26 A | 03-Jun-26 A | 0.00 | 0.00 | 0.00 | -12 |
| MLTX-02-005-EN | Shop DWG Approval for Water Supply Details | 21 | 100% | 100% | 23-Apr-26 | 17-May-26 | 03-Jun-26 A | 03-Jun-26 A | 0.00 | 0.00 | 0.00 | -12 |
| MLTX-02-005-EN | Shop DWG Approval for Drainage Layout | 21 | 100% | 100% | 23-Apr-26 | 17-May-26 | 30-Mar-26 A | 04-Jun-26 A | 0.00 | 0.00 | 0.00 | -13 |
| MLTX-02-005-EN | Shop DWG Approval for Drainage Details | 21 | 100% | 100% | 23-Apr-26 | 17-May-26 | 30-Mar-26 A | 04-Jun-26 A | 0.00 | 0.00 | 0.00 | -13 |
| MLTX-02-005-EN | Shop DWG Approval for Duct Routing Layout | 21 | 100% | 100% | 23-Apr-26 | 17-May-26 | 24-Mar-26 A | 04-Apr-26 A | 0.00 | 0.00 | 0.00 | 37 |
| MLTX-02-005-EN | Shop DWG Approval for Diffusers Layout | 21 | 100% | 100% | 23-Apr-26 | 17-May-26 | 30-Jul-26 A | 30-Jul-26 A | 0.00 | 0.00 | 0.00 | -61 |
| **ELECTRICAL WORKS** | | 51 | 0% | 0% | 16-Apr-26 | 20-May-26 | 24-Mar-26 A | 30-Jul-26 A | 0.00 | 0.00 | 0.00 | -58 |
| MLTX-02-005-EN | Shop DWG Approval for Lighting Layout | 21 | 100% | 100% | 23-Apr-26 | 17-May-26 | 24-Mar-26 A | 04-Apr-26 A | 0.00 | 0.00 | 0.00 | 37 |
| MLTX-02-005-EN | Shop DWG Approval for Power Layout | 21 | 100% | 100% | 23-Apr-26 | 17-May-26 | 24-Mar-26 A | 04-Apr-26 A | 0.00 | 0.00 | 0.00 | 37 |
| MLTX-02-005-EN | Shop DWG Approval for Power Single Line Diagram | 21 | 100% | 100% | 23-Apr-26 | 17-May-26 | 30-Jul-26 A | 30-Jul-26 A | 0.00 | 0.00 | 0.00 | -61 |
| MLTX-02-005-EN | Shop DWG Approval for Panel Board Schedules | 30 | 100% | 100% | 16-Apr-26 | 20-May-26 | 22-Jul-26 A | 22-Jul-26 A | 0.00 | 0.00 | 0.00 | -51 |
| MLTX-02-005-EN | Shop DWG Approval for Lighting Installation Details | 21 | 100% | 100% | 23-Apr-26 | 17-May-26 | 24-Mar-26 A | 04-Apr-26 A | 0.00 | 0.00 | 0.00 | 37 |
| MLTX-02-005-EN | Shop DWG Approval for Power Installation Details | 30 | 100% | 100% | 16-Apr-26 | 20-May-26 | 24-Mar-26 A | 04-Apr-26 A | 0.00 | 0.00 | 0.00 | 40 |
| MLTX-02-005-EN | Shop DWG Approval for Cable Tray Installation Details | 30 | 100% | 100% | 16-Apr-26 | 20-May-26 | 30-Jul-26 A | 30-Jul-26 A | 0.00 | 0.00 | 0.00 | -58 |
| MLTX-02-005-EN | Shop DWG Approval for Manhole & Ductbank Details | 30 | 100% | 100% | 16-Apr-26 | 20-May-26 | 30-Jul-26 A | 30-Jul-26 A | 0.00 | 0.00 | 0.00 | -58 |
| MLTX-02-005-EN | Shop DWG Approval for Grounding Details | 30 | 100% | 100% | 16-Apr-26 | 20-May-26 | 24-Mar-26 A | 04-Apr-26 A | 0.00 | 0.00 | 0.00 | 40 |
| MLTX-02-005-EN | Shop DWG Approval for Lightning Protection Details | 30 | 100% | 100% | 16-Apr-26 | 20-May-26 | 24-Mar-26 A | 04-Apr-26 A | 0.00 | 0.00 | 0.00 | 40 |
| MLTX-02-005-EN | Shop DWG Approval for Fire Alarm Installation Details | 30 | 100% | 100% | 16-Apr-26 | 20-May-26 | 24-Mar-26 A | 04-Apr-26 A | 0.00 | 0.00 | 0.00 | 40 |
| MLTX-02-005-EN | Shop DWG Approval for CCTV Details | 30 | 100% | 100% | 16-Apr-26 | 20-May-26 | 30-Jul-26 A | 30-Jul-26 A | 0.00 | 0.00 | 0.00 | -58 |
| MLTX-02-005-EN | Shop DWG Approval for Grounding Layout | 30 | 100% | 100% | 16-Apr-26 | 20-May-26 | 24-Mar-26 A | 04-Apr-26 A | 0.00 | 0.00 | 0.00 | 40 |
| MLTX-02-005-EN | Shop DWG Approval for Lightning Protection System Layout | 30 | 100% | 100% | 16-Apr-26 | 20-May-26 | 24-Mar-26 A | 04-Apr-26 A | 0.00 | 0.00 | 0.00 | 40 |
| MLTX-02-005-EN | Shop DWG Approval for Fire Alarm Layout | 30 | 100% | 100% | 16-Apr-26 | 20-May-26 | 24-Mar-26 A | 04-Apr-26 A | 0.00 | 0.00 | 0.00 | 40 |
| MLTX-02-005-EN | Shop DWG Approval for Fire Alarm Riser Diagram | 30 | 100% | 100% | 16-Apr-26 | 20-May-26 | 24-Mar-26 A | 04-Apr-26 A | 0.00 | 0.00 | 0.00 | 40 |
| MLTX-02-005-EN | Shop DWG Approval for CCTV Layout | 30 | 100% | 100% | 16-Apr-26 | 20-May-26 | 30-Jul-26 A | 30-Jul-26 A | 0.00 | 0.00 | 0.00 | -58 |
| MLTX-02-005-EN | Shop DWG Approval for CCTV Riser Diagram | 30 | 100% | 100% | 16-Apr-26 | 20-May-26 | 30-Jul-26 A | 30-Jul-26 A | 0.00 | 0.00 | 0.00 | -58 |
| MLTX-02-005-EN | Shop DWG Approval for Telephone & Data Layout | 21 | 100% | 100% | 23-Apr-26 | 17-May-26 | 24-Mar-26 A | 04-Apr-26 A | 0.00 | 0.00 | 0.00 | 37 |
| MLTX-02-005-EN | Shop DWG Approval for Telephone & Data Riser Diagram | 21 | 100% | 100% | 23-Apr-26 | 17-May-26 | 30-Jul-26 A | 30-Jul-26 A | 0.00 | 0.00 | 0.00 | -61 |
| **SHOP DRAWINGS APPROVAL FOR PLAYGROUND WORKS** | | 101 | 0% | 0% | 30-Mar-26 | 20-Sep-26 | 15-Mar-26 A | 16-Nov-26 | 0.00 | 0.00 | 0.00 | -48 |
| **ARCHITECTURE WORKS** | | 36 | 0% | 0% | 30-Mar-26 | 10-May-26 | 15-Mar-26 A | 24-May-26 A | 0.00 | 0.00 | 0.00 | -12 |
| MLTX-02-005-EN | Shop DWG Approval for Playground Plan/Layout | 15 | 100% | 100% | 30-Mar-26 | 15-Apr-26 | 15-Mar-26 A | 29-Mar-26 A | 0.00 | 0.00 | 0.00 | 15 |
| MLTX-02-005-EN | Shop DWG Approval for Furniture & Marking | 30 | 100% | 100% | 30-Mar-26 | 03-May-26 | 15-Mar-26 A | 14-May-26 A | 0.00 | 0.00 | 0.00 | -10 |
| MLTX-02-005-EN | Shop DWG Approval for Sections | 20 | 100% | 100% | 30-Mar-26 | 21-Apr-26 | 15-Mar-26 A | 29-Mar-26 A | 0.00 | 0.00 | 0.00 | 20 |
| MLTX-02-005-EN | Shop DWG Approval for Interlock Pattern Plan | 30 | 100% | 100% | 06-Apr-26 | 10-May-26 | 15-Mar-26 A | 29-Mar-26 A | 0.00 | 0.00 | 0.00 | 36 |
| MLTX-02-005-EN | Shop DWG Approval for Doors/Windows Schedule | 20 | 100% | 100% | 06-Apr-26 | 28-Apr-26 | 15-Mar-26 A | 24-May-26 A | 0.00 | 0.00 | 0.00 | -22 |
| MLTX-02-005-EN | Shop DWG Approval for Dome Internal Layout | 30 | 100% | 100% | 06-Apr-26 | 10-May-26 | 15-Mar-26 A | 24-May-26 A | 0.00 | 0.00 | 0.00 | -12 |
| **STRUCTURE WORKS** | | 35 | 0% | 0% | 30-Apr-26 | 24-May-26 | 24-Mar-26 A | 16-Jul-26 A | 0.00 | 0.00 | 0.00 | -43 |
| MLTX-02-005-EN | Shop DWG Approval for Air Dome System | 21 | 100% | 100% | 30-Apr-26 | 24-May-26 | 24-Mar-26 A | 16-May-26 A | 0.00 | 0.00 | 0.00 | 7 |
| MLTX-02-005-EN | Shop DWG Approval for Foundation of Air Dome | 21 | 100% | 100% | 30-Apr-26 | 24-May-26 | 16-Jul-26 A | 16-Jul-26 A | 0.00 | 0.00 | 0.00 | -43 |
| MLTX-02-005-EN | Shop DWG Approval for Foundation of Air Dome | 21 | 100% | 100% | 30-Apr-26 | 24-May-26 | 16-Jul-26 A | 16-Jul-26 A | 0.00 | 0.00 | 0.00 | -43 |
| MLTX-02-005-EN | Shop DWG Approval for Anchor Bolt Layout of Air Dome | 21 | 100% | 100% | 30-Apr-26 | 24-May-26 | 16-Jul-26 A | 16-Jul-26 A | 0.00 | 0.00 | 0.00 | -43 |
| **AIR DOME SYSTEM** | | 21 | 0% | 0% | 30-Apr-26 | 24-May-26 | 24-Mar-26 A | 25-May-26 A | 0.00 | 0.00 | 0.00 | -1 |
| MLTX-02-005-EN | Shop DWG Approval for Air Dome Structural Layout | 21 | 100% | 100% | 30-Apr-26 | 24-May-26 | 24-Mar-26 A | 16-May-26 A | 0.00 | 0.00 | 0.00 | 7 |
| MLTX-02-005-EN | Shop DWG Approval for Membrane Panel Layout | 21 | 100% | 100% | 30-Apr-26 | 24-May-26 | 24-Mar-26 A | 25-May-26 A | 0.00 | 0.00 | 0.00 | -1 |
| MLTX-02-005-EN | Shop DWG Approval for Cable Tension Layout | 21 | 100% | 100% | 30-Apr-26 | 24-May-26 | 24-Mar-26 A | 25-May-26 A | 0.00 | 0.00 | 0.00 | -1 |
| MLTX-02-005-EN | Shop DWG Approval for Airlock Door Details | 21 | 100% | 100% | 30-Apr-26 | 24-May-26 | 24-Mar-26 A | 25-May-26 A | 0.00 | 0.00 | 0.00 | -1 |
| MLTX-02-005-EN | Shop DWG Approval for Emergency Exit Details | 21 | 100% | 100% | 30-Apr-26 | 24-May-26 | 24-Mar-26 A | 25-May-26 A | 0.00 | 0.00 | 0.00 | -1 |
| **SPORTS EQUIPMENT** | | 68 | 0% | 0% | 30-Apr-26 | 07-Jun-26 | 20-Jul-26 A | 22-Oct-26 | 0.00 | 0.00 | 0.00 | -117 |
| MLTX-02-005-EN | Shop DWG Approval for Football Turf Installation | 21 | 100% | 0% | 30-Apr-26 | 24-May-26 | 29-Sep-26 | 22-Oct-26 | 0.00 | 0.00 | 0.00 | -126 |
| MLTX-02-005-EN | Shop DWG Approval for Basketball Court Marking | 30 | 100% | 100% | 30-Apr-26 | 07-Jun-26 | 25-Aug-26 A | 25-Aug-26 A | 0.00 | 0.00 | 0.00 | -68 |
| MLTX-02-005-EN | Shop DWG Approval for Padel Court Structure | 30 | 100% | 100% | 30-Apr-26 | 07-Jun-26 | 20-Jul-26 A | 20-Jul-26 A | 0.00 | 0.00 | 0.00 | -37 |
| **MECHANCAL WORKS** | | 21 | 0% | 0% | 27-Aug-26 | 20-Sep-26 | 24-Oct-26 | 16-Nov-26 | 0.00 | 0.00 | 0.00 | -48 |
| MLTX-02-005-EN | Shop DWG Approval for HVAC Plan | 21 | 100% | 0% | 27-Aug-26 | 20-Sep-26 | 24-Oct-26 | 16-Nov-26 | 0.00 | 0.00 | 0.00 | -48 |
| MLTX-02-005-EN | Shop DWG Approval for Exhaust Air Plan | 21 | 100% | 0% | 27-Aug-26 | 20-Sep-26 | 24-Oct-26 | 16-Nov-26 | 0.00 | 0.00 | 0.00 | -48 |
| **ELECTRICAL WORKS** | | 66 | 0% | 0% | 27-Aug-26 | 20-Sep-26 | 25-Aug-26 A | 16-Nov-26 | 0.00 | 0.00 | 0.00 | -48 |

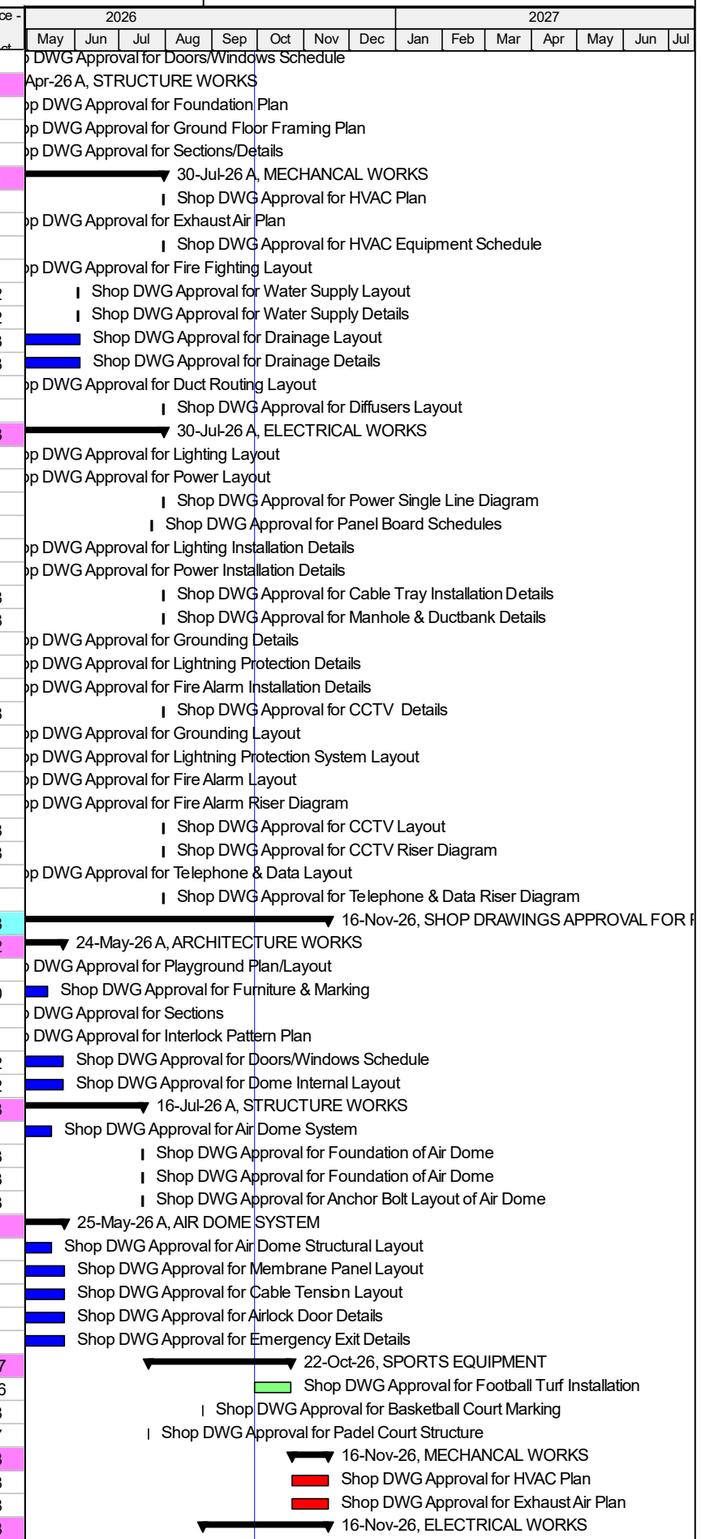




© Oracle Corporation

# MLTX-02-005 - Playground Initiative for Eastern Region (Arar-Hasa osis -Dammam)

**Updateded schedule**
**D.D 28-09-2026**

| Activity ID | Activity Name | Original Duration | Schedule % Complete | Performance % Complete | BL Project Start | BL Project Finish | Start | Finish | Planned Value Cost | Earned Value Cost | Budgeted Total Cost | Variance - BL Project |
|---|---|---|---|---|---|---|---|---|---|---|---|---|
| MLTX-02-005-EN | Shop DWG Approval for Lighting Layout | 21 | 100% | 0% | 27-Aug-26 | 20-Sep-26 | 24-Oct-26 | 16-Nov-26 | 0.00 | 0.00 | 0.00 | -48 |
| MLTX-02-005-EN | Shop DWG Approval for Power Layout | 21 | 100% | 0% | 27-Aug-26 | 20-Sep-26 | 24-Oct-26 | 16-Nov-26 | 0.00 | 0.00 | 0.00 | -48 |
| MLTX-02-005-EN | Shop DWG Approval for Power Single Line Diagram | 21 | 100% | 0% | 27-Aug-26 | 20-Sep-26 | 24-Oct-26 | 16-Nov-26 | 0.00 | 0.00 | 0.00 | -48 |
| MLTX-02-005-EN | Shop DWG Approval for Panel Board Schedules | 21 | 100% | 0% | 27-Aug-26 | 20-Sep-26 | 24-Oct-26 | 16-Nov-26 | 0.00 | 0.00 | 0.00 | -48 |
| MLTX-02-005-EN | Shop DWG Approval for Power Installation Details | 21 | 100% | 0% | 27-Aug-26 | 20-Sep-26 | 24-Oct-26 | 16-Nov-26 | 0.00 | 0.00 | 0.00 | -48 |
| MLTX-02-005-EN | Shop DWG Approval for CCTV Details | 21 | 100% | 100% | 27-Aug-26 | 20-Sep-26 | 25-Aug-26 A | 25-Aug-26 A | 0.00 | 0.00 | 0.00 | 22 |
| MLTX-02-005-EN | Shop DWG Approval for CCTV Layout | 21 | 100% | 100% | 27-Aug-26 | 20-Sep-26 | 25-Aug-26 A | 25-Aug-26 A | 0.00 | 0.00 | 0.00 | 22 |
| MLTX-02-005-EN | Shop DWG Approval for CCTV Riser Diagram | 21 | 100% | 100% | 27-Aug-26 | 20-Sep-26 | 25-Aug-26 A | 25-Aug-26 A | 0.00 | 0.00 | 0.00 | 22 |
| **SHOP DRAWINGS APPROVAL FOR LANDSCAPE WORKS** | | 72 | 0% | 0% | 30-Mar-26 | 20-May-26 | 15-Mar-26 A | 30-Jul-26 A | 0.00 | 0.00 | 0.00 | -58 |
| **ARCHITECTURE WORKS** | | 30 | 0% | 0% | 30-Mar-26 | 03-May-26 | 15-Mar-26 A | 19-May-26 A | 0.00 | 0.00 | 0.00 | -14 |
| MLTX-02-005-EN | Shop DWG Approval for Landscape Layout | 21 | 100% | 100% | 06-Apr-26 | 29-Apr-26 | 15-Mar-26 A | 29-Mar-26 A | 0.00 | 0.00 | 0.00 | 27 |
| MLTX-02-005-EN | Shop DWG Approval for Hardscape Plan | 21 | 100% | 100% | 06-Apr-26 | 29-Apr-26 | 15-Mar-26 A | 29-Mar-26 A | 0.00 | 0.00 | 0.00 | 27 |
| MLTX-02-005-EN | Shop DWG Approval for Planting Plan | 15 | 100% | 100% | 16-Apr-26 | 03-May-26 | 24-Mar-26 A | 19-May-26 A | 0.00 | 0.00 | 0.00 | -14 |
| MLTX-02-005-EN | Shop DWG Approval for Landscape Details | 21 | 100% | 100% | 30-Mar-26 | 22-Apr-26 | 15-Mar-26 A | 29-Mar-26 A | 0.00 | 0.00 | 0.00 | 21 |
| **MECHANCAL WORKS** | | 30 | 0% | 0% | 16-Apr-26 | 20-May-26 | 08-Jul-26 A | 08-Jul-26 A | 0.00 | 0.00 | 0.00 | -39 |
| MLTX-02-005-EN | Shop DWG Approval for Irrigation Details | 30 | 100% | 100% | 16-Apr-26 | 20-May-26 | 08-Jul-26 A | 08-Jul-26 A | 0.00 | 0.00 | 0.00 | -39 |
| MLTX-02-005-EN | Shop DWG Approval for Irrigation Layout | 30 | 100% | 100% | 16-Apr-26 | 20-May-26 | 08-Jul-26 A | 08-Jul-26 A | 0.00 | 0.00 | 0.00 | -39 |
| **ELECTRICAL WORKS** | | 30 | 0% | 0% | 16-Apr-26 | 20-May-26 | 30-Jul-26 A | 30-Jul-26 A | 0.00 | 0.00 | 0.00 | -58 |
| MLTX-02-005-EN | Shop DWG Approval for Lighting General Arrangement | 30 | 100% | 100% | 16-Apr-26 | 20-May-26 | 30-Jul-26 A | 30-Jul-26 A | 0.00 | 0.00 | 0.00 | -58 |
| MLTX-02-005-EN | Shop DWG Approval for Lighting Network Layout | 30 | 100% | 100% | 16-Apr-26 | 20-May-26 | 30-Jul-26 A | 30-Jul-26 A | 0.00 | 0.00 | 0.00 | -58 |
| MLTX-02-005-EN | Shop DWG Approval for Lighting Details | 30 | 100% | 100% | 16-Apr-26 | 20-May-26 | 30-Jul-26 A | 30-Jul-26 A | 0.00 | 0.00 | 0.00 | -58 |
| MLTX-02-005-EN | Shop DWG Approval for Lighting Single Line Diagram | 30 | 100% | 100% | 16-Apr-26 | 20-May-26 | 30-Jul-26 A | 30-Jul-26 A | 0.00 | 0.00 | 0.00 | -58 |
| **METHOD STATEMENTS** | | 94 | 0% | 0% | 08-Mar-26 | 27-Jun-26 | 08-Mar-26 A | 12-Sep-26 A | 0.00 | 0.00 | 0.00 | -66 |
| **METHOD STATEMENT SUBMITTAL** | | 60 | 0% | 0% | 08-Mar-26 | 19-May-26 | 08-Mar-26 A | 04-Jun-26 A | 0.00 | 0.00 | 0.00 | -11 |
| **CIVIL WORKS** | | 21 | 0% | 0% | 08-Mar-26 | 04-Apr-26 | 09-Mar-26 A | 14-Mar-26 A | 0.00 | 0.00 | 0.00 | 15 |
| MLTX-02-005-EN-7 | Preparation & Submission of Method Statement for | 15 | 100% | 100% | 08-Mar-26 | 28-Mar-26 | 09-Mar-26 A | 14-Mar-26 A | 0.00 | 0.00 | 0.00 | 9 |
| MLTX-02-005-EN-7 | Preparation & Submission of Method Statement for Concrete | 21 | 100% | 100% | 08-Mar-26 | 04-Apr-26 | 09-Mar-26 A | 14-Mar-26 A | 0.00 | 0.00 | 0.00 | 15 |
| MLTX-02-005-EN-7 | Preparation & Submission of Method Statement for | 21 | 100% | 100% | 08-Mar-26 | 04-Apr-26 | 09-Mar-26 A | 14-Mar-26 A | 0.00 | 0.00 | 0.00 | 15 |
| **ARCHITECTURE WORKS** | | 30 | 0% | 0% | 08-Mar-26 | 14-Apr-26 | 08-Mar-26 A | 02-Jun-26 A | 0.00 | 0.00 | 0.00 | -39 |
| MLTX-02-005-EN-7 | Preparation & Submission of Method Statement for Plastering | 15 | 100% | 100% | 08-Mar-26 | 28-Mar-26 | 09-Mar-26 A | 14-Mar-26 A | 0.00 | 0.00 | 0.00 | 9 |
| MLTX-02-005-EN-7 | Preparation & Submission of Method Statement for | 21 | 100% | 100% | 08-Mar-26 | 04-Apr-26 | 08-Mar-26 A | 11-May-26 A | 0.00 | 0.00 | 0.00 | -32 |
| MLTX-02-005-EN-8 | Preparation & Submission of Method Statement for Tilling | 30 | 100% | 100% | 08-Mar-26 | 14-Apr-26 | 08-Mar-26 A | 17-May-26 A | 0.00 | 0.00 | 0.00 | -28 |
| MLTX-02-005-EN-8 | Preparation & Submission of Method Statement for | 30 | 100% | 100% | 08-Mar-26 | 14-Apr-26 | 08-Mar-26 A | 02-Jun-26 A | 0.00 | 0.00 | 0.00 | -39 |
| MLTX-02-005-EN-8 | Preparation & Submission of Method Statement for | 30 | 100% | 100% | 08-Mar-26 | 14-Apr-26 | 08-Mar-26 A | 02-Jun-26 A | 0.00 | 0.00 | 0.00 | -39 |
| MLTX-02-005-EN-8 | Preparation & Submission of Method Statement for | 21 | 100% | 100% | 08-Mar-26 | 04-Apr-26 | 08-Mar-26 A | 24-May-26 A | 0.00 | 0.00 | 0.00 | -43 |
| MLTX-02-005-EN-8 | Preparation & Submission of Method Statement for Parking | 30 | 100% | 100% | 08-Mar-26 | 14-Apr-26 | 08-Mar-26 A | 24-May-26 A | 0.00 | 0.00 | 0.00 | -34 |
| MLTX-02-005-EN-8 | Preparation & Submission of Method Statement for Soft | 21 | 100% | 100% | 08-Mar-26 | 04-Apr-26 | 08-Mar-26 A | 02-Jun-26 A | 0.00 | 0.00 | 0.00 | -48 |
| MLTX-02-005-EN-8 | Preparation & Submission of Method Statement for Fence | 30 | 100% | 100% | 08-Mar-26 | 14-Apr-26 | 08-Mar-26 A | 02-Jun-26 A | 0.00 | 0.00 | 0.00 | -39 |
| MLTX-02-005-EN-8 | Preparation & Submission of Method Statement for Air Dome | 30 | 100% | 100% | 08-Mar-26 | 14-Apr-26 | 08-Mar-26 A | 02-Jun-26 A | 0.00 | 0.00 | 0.00 | -39 |
| MLTX-02-005-EN-8 | Preparation & Submission of Method Statement for Metal | 21 | 100% | 100% | 08-Mar-26 | 04-Apr-26 | 08-Mar-26 A | 02-Jun-26 A | 0.00 | 0.00 | 0.00 | -48 |
| MLTX-02-005-EN-8 | Preparation & Submission of Method Statement for Partitions | 21 | 100% | 100% | 08-Mar-26 | 04-Apr-26 | 08-Mar-26 A | 02-Jun-26 A | 0.00 | 0.00 | 0.00 | -48 |
| MLTX-02-005-EN-8 | Preparation & Submission of Method Statement for Gypsum | 21 | 100% | 100% | 08-Mar-26 | 04-Apr-26 | 08-Mar-26 A | 02-Jun-26 A | 0.00 | 0.00 | 0.00 | -48 |
| **MECHANICAL WORKS** | | 27 | 0% | 0% | 29-Mar-26 | 28-Apr-26 | 14-Mar-26 A | 04-Jun-26 A | 0.00 | 0.00 | 0.00 | -29 |
| MLTX-02-005-EN-8 | Preparation & Submission of Method Statement for | 21 | 100% | 100% | 29-Mar-26 | 21-Apr-26 | 14-Mar-26 A | 04-May-26 A | 0.00 | 0.00 | 0.00 | -11 |
| MLTX-02-005-EN-8 | Preparation & Submission of Method Statement for Water | 21 | 100% | 100% | 05-Apr-26 | 28-Apr-26 | 14-Mar-26 A | 04-May-26 A | 0.00 | 0.00 | 0.00 | -5 |
| MLTX-02-005-EN-8 | Preparation & Submission of Method Statement for Fire | 21 | 100% | 100% | 05-Apr-26 | 28-Apr-26 | 14-Mar-26 A | 04-Jun-26 A | 0.00 | 0.00 | 0.00 | -29 |
| MLTX-02-005-EN-8 | Preparation & Submission of Method Statement for Irrigation | 15 | 100% | 100% | 29-Mar-26 | 14-Apr-26 | 14-Mar-26 A | 04-Jun-26 A | 0.00 | 0.00 | 0.00 | -41 |
| MLTX-02-005-EN-8 | Preparation & Submission of Method Statement for HVAC | 21 | 100% | 100% | 05-Apr-26 | 28-Apr-26 | 14-Mar-26 A | 04-Jun-26 A | 0.00 | 0.00 | 0.00 | -29 |
| **ELECTRICAL WORKS** | | 39 | 0% | 0% | 05-Apr-26 | 19-May-26 | 14-Mar-26 A | 11-May-26 A | 0.00 | 0.00 | 0.00 | 7 |
| MLTX-02-005-EN-7 | Preparation & Submission of Method Statement for Electrical | 21 | 100% | 100% | 05-Apr-26 | 28-Apr-26 | 14-Mar-26 A | 11-May-26 A | 0.00 | 0.00 | 0.00 | -11 |
| MLTX-02-005-EN-7 | Preparation & Submission of Method Statement for Lighting | 21 | 100% | 100% | 05-Apr-26 | 28-Apr-26 | 14-Mar-26 A | 11-May-26 A | 0.00 | 0.00 | 0.00 | -11 |
| MLTX-02-005-EN-8 | Preparation & Submission of Method Statement for | 30 | 100% | 100% | 15-Apr-26 | 19-May-26 | 14-Mar-26 A | 11-May-26 A | 0.00 | 0.00 | 0.00 | 7 |
| MLTX-02-005-EN-8 | Preparation & Submission of Method Statement for CCTV | 30 | 100% | 100% | 15-Apr-26 | 19-May-26 | 14-Mar-26 A | 11-May-26 A | 0.00 | 0.00 | 0.00 | 7 |
| MLTX-02-005-EN-8 | Preparation & Submission of Method Statement for Lighting | 21 | 100% | 100% | 05-Apr-26 | 28-Apr-26 | 14-Mar-26 A | 11-May-26 A | 0.00 | 0.00 | 0.00 | -11 |
| MLTX-02-005-EN-8 | Preparation & Submission of Method Statement for | 21 | 100% | 100% | 05-Apr-26 | 28-Apr-26 | 14-Mar-26 A | 11-May-26 A | 0.00 | 0.00 | 0.00 | -11 |
| MLTX-02-005-EN-8 | Preparation & Submission of Method Statement for Panel | 21 | 100% | 100% | 05-Apr-26 | 28-Apr-26 | 14-Mar-26 A | 11-May-26 A | 0.00 | 0.00 | 0.00 | -11 |
| **METHOD STATEMENT APPROVAL** | | 79 | 0% | 0% | 29-Mar-26 | 27-Jun-26 | 14-Mar-26 A | 12-Sep-26 A | 0.00 | 0.00 | 0.00 | -66 |
| **CIVIL WORKS** | | 36 | 0% | 0% | 29-Mar-26 | 09-May-26 | 14-Mar-26 A | 30-Apr-26 A | 0.00 | 0.00 | 0.00 | 7 |
| MLTX-02-005-EN-1 | Approval of Method Statement for Earthwork | 15 | 100% | 100% | 29-Mar-26 | 14-Apr-26 | 14-Mar-26 A | 30-Apr-26 A | 0.00 | 0.00 | 0.00 | -14 |
| MLTX-02-005-EN-1 | Approval of Method Statement for Concrete Works | 30 | 100% | 100% | 05-Apr-26 | 09-May-26 | 14-Mar-26 A | 30-Apr-26 A | 0.00 | 0.00 | 0.00 | 7 |
| MLTX-02-005-EN-1 | Approval of Method Statement for Waterproofing | 21 | 100% | 100% | 05-Apr-26 | 28-Apr-26 | 14-Mar-26 A | 30-Apr-26 A | 0.00 | 0.00 | 0.00 | -2 |
| **ARCHITECTURE WORKS** | | 79 | 0% | 0% | 29-Mar-26 | 19-May-26 | 14-Mar-26 A | 12-Sep-26 A | 0.00 | 0.00 | 0.00 | -96 |
| MLTX-02-005-EN-1 | Approval of Method Statement for Plastering Works | 30 | 100% | 100% | 29-Mar-26 | 02-May-26 | 14-Mar-26 A | 30-Apr-26 A | 0.00 | 0.00 | 0.00 | 1 |
| MLTX-02-005-EN-1 | Approval of Method Statement for Masonary Works | 30 | 100% | 100% | 05-Apr-26 | 09-May-26 | 14-Mar-26 A | 21-May-26 A | 0.00 | 0.00 | 0.00 | -11 |

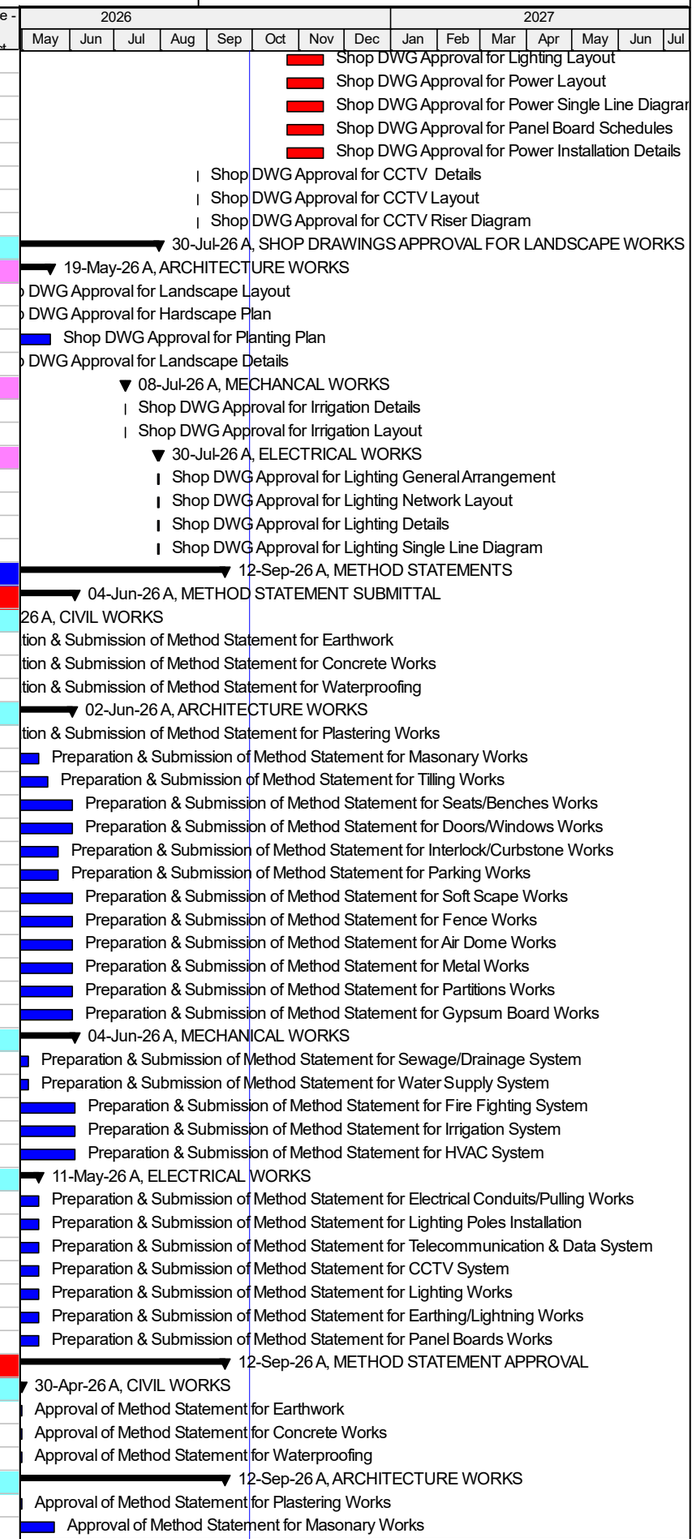





© Oracle Corporation

# MLTX-02-005 - Playground Initiative for Eastern Region (Arar-Hasa osis -Dammam)

**Updateded schedule**
**D.D 28-09-2026**

| Activity ID | Activity Name | Original Duration | Schedule % Complete | Performance % Complete | BL Project Start | BL Project Finish | Start | Finish | Planned Value Cost | Earned Value Cost | Budgeted Total Cost | Variance - BL Project |
|---|---|---|---|---|---|---|---|---|---|---|---|---|
| MLTX-02-005-EN-1 | Approval of Method Statement for Tilling Works | 30 | 100% | 100% | 15-Apr-26 | 19-May-26 | 14-Mar-26 A | 21-May-26 A | 0.00 | 0.00 | 0.00 | -2 |
| MLTX-02-005-EN-1 | Approval of Method Statement for Seats/Benches Works | 30 | 100% | 100% | 15-Apr-26 | 19-May-26 | 12-Sep-26 A | 12-Sep-26 A | 0.00 | 0.00 | 0.00 | -96 |
| MLTX-02-005-EN-1 | Approval of Method Statement for Doors/Windows Works | 30 | 100% | 100% | 15-Apr-26 | 19-May-26 | 12-Sep-26 A | 12-Sep-26 A | 0.00 | 0.00 | 0.00 | -96 |
| MLTX-02-005-EN-1 | Approval of Method Statement for Interlock/Curbstone Works | 30 | 100% | 100% | 05-Apr-26 | 09-May-26 | 15-Aug-26 A | 15-Aug-26 A | 0.00 | 0.00 | 0.00 | -81 |
| MLTX-02-005-EN-1 | Approval of Method Statement for Parking Works | 30 | 100% | 100% | 15-Apr-26 | 19-May-26 | 26-Aug-26 A | 26-Aug-26 A | 0.00 | 0.00 | 0.00 | -82 |
| MLTX-02-005-EN-1 | Approval of Method Statement for Soft Scape Works | 30 | 100% | 100% | 05-Apr-26 | 09-May-26 | 12-Sep-26 A | 12-Sep-26 A | 0.00 | 0.00 | 0.00 | -105 |
| MLTX-02-005-EN-1 | Approval of Method Statement for Fence Works | 30 | 100% | 100% | 15-Apr-26 | 19-May-26 | 10-Aug-26 A | 10-Aug-26 A | 0.00 | 0.00 | 0.00 | -68 |
| MLTX-02-005-EN-1 | Approval of Method Statement for Air Dome Works | 30 | 100% | 100% | 15-Apr-26 | 19-May-26 | 11-Jul-26 A | 22-Jul-26 A | 0.00 | 0.00 | 0.00 | -52 |
| MLTX-02-005-EN-1 | Approval of Method Statement for Partitions Works | 30 | 100% | 100% | 05-Apr-26 | 09-May-26 | 12-Sep-26 A | 12-Sep-26 A | 0.00 | 0.00 | 0.00 | -105 |
| MLTX-02-005-EN-1 | Approval of Method Statement for Gypsum Board Works | 30 | 100% | 100% | 05-Apr-26 | 09-May-26 | 20-Aug-26 A | 20-Aug-26 A | 0.00 | 0.00 | 0.00 | -86 |
| **MECHANICAL WORKS** | | 50 | 0% | 0% | 15-Apr-26 | 23-May-26 | 02-Jun-26 A | 26-Aug-26 A | 0.00 | 0.00 | 0.00 | -79 |
| MLTX-02-005-EN-1 | Approval of Method Statement for Sewage/Drainage System | 21 | 100% | 100% | 22-Apr-26 | 16-May-26 | 09-Jun-26 A | 09-Jun-26 A | 0.00 | 0.00 | 0.00 | -18 |
| MLTX-02-005-EN-1 | Approval of Method Statement for Water Supply System | 21 | 100% | 100% | 29-Apr-26 | 23-May-26 | 02-Jun-26 A | 02-Jun-26 A | 0.00 | 0.00 | 0.00 | -6 |
| MLTX-02-005-EN-1 | Approval of Method Statement for Fire Fighting System | 21 | 100% | 100% | 29-Apr-26 | 23-May-26 | 26-Aug-26 A | 26-Aug-26 A | 0.00 | 0.00 | 0.00 | -79 |
| MLTX-02-005-EN-1 | Approval of Method Statement for Irrigation System | 15 | 100% | 100% | 15-Apr-26 | 02-May-26 | 28-Jun-26 A | 28-Jun-26 A | 0.00 | 0.00 | 0.00 | -46 |
| MLTX-02-005-EN-1 | Approval of Method Statement for HVAC System | 21 | 100% | 100% | 29-Apr-26 | 23-May-26 | 25-Aug-26 A | 25-Aug-26 A | 0.00 | 0.00 | 0.00 | -78 |
| **ELECTRICAL WORKS** | | 58 | 0% | 0% | 29-Apr-26 | 27-Jun-26 | 12-Jul-26 A | 26-Aug-26 A | 0.00 | 0.00 | 0.00 | -52 |
| MLTX-02-005-EN-1 | Approval of Method Statement for Electrical Conduits/Pulling | 21 | 100% | 100% | 29-Apr-26 | 23-May-26 | 12-Jul-26 A | 16-Jul-26 A | 0.00 | 0.00 | 0.00 | -44 |
| MLTX-02-005-EN-1 | Approval of Method Statement for Lighting Poles Installation | 21 | 100% | 100% | 29-Apr-26 | 23-May-26 | 26-Aug-26 A | 26-Aug-26 A | 0.00 | 0.00 | 0.00 | -79 |
| MLTX-02-005-EN-1 | Approval of Method Statement for Telecommunication & Data | 30 | 100% | 100% | 20-May-26 | 27-Jun-26 | 10-Aug-26 A | 10-Aug-26 A | 0.00 | 0.00 | 0.00 | -38 |
| MLTX-02-005-EN-1 | Approval of Method Statement for CCTV System | 30 | 100% | 100% | 20-May-26 | 27-Jun-26 | 10-Aug-26 A | 10-Aug-26 A | 0.00 | 0.00 | 0.00 | -38 |
| MLTX-02-005-EN-1 | Approval of Method Statement for Lighting Works | 21 | 100% | 100% | 29-Apr-26 | 23-May-26 | 10-Aug-26 A | 10-Aug-26 A | 0.00 | 0.00 | 0.00 | -65 |
| MLTX-02-005-EN-1 | Approval of Method Statement for Earthing/Lightning Works | 21 | 100% | 100% | 29-Apr-26 | 23-May-26 | 10-Aug-26 A | 10-Aug-26 A | 0.00 | 0.00 | 0.00 | -65 |
| MLTX-02-005-EN-1 | Approval of Method Statement for Panel Boards Works | 21 | 100% | 100% | 29-Apr-26 | 23-May-26 | 12-Jul-26 A | 22-Jul-26 A | 0.00 | 0.00 | 0.00 | -49 |
| **PRE-QUALIFICATION & MATERIAL** | | 94 | 0% | 0% | 08-Mar-26 | 13-Jun-26 | 08-Mar-26 A | 12-Sep-26 A | 0.00 | 0.00 | 0.00 | -78 |
| **PRE-QUALIFICATION** | | 45 | 0% | 0% | 08-Mar-26 | 02-May-26 | 08-Mar-26 A | 07-Jun-26 A | 0.00 | 0.00 | 0.00 | -28 |
| **TOILET/SERVICE WORKS** | | 45 | 0% | 0% | 08-Mar-26 | 02-May-26 | 08-Mar-26 A | 07-Jun-26 A | 0.00 | 0.00 | 0.00 | -28 |
| **STEEL REINFORCEMENT** | | 30 | 0% | 0% | 08-Mar-26 | 14-Apr-26 | 09-Mar-26 A | 19-Mar-26 A | 0.00 | 0.00 | 0.00 | 19 |
| MLTX-02-005-EN | Pre-Qualification Approval for Steel Reinforcement | 15 | 100% | 100% | 29-Mar-26 | 14-Apr-26 | 12-Mar-26 A | 19-Mar-26 A | 0.00 | 0.00 | 0.00 | 19 |
| MLTX-02-005-EN | Pre-Qualification Submittal for Steel Reinforcement | 15 | 100% | 100% | 08-Mar-26 | 28-Mar-26 | 09-Mar-26 A | 11-Mar-26 A | 0.00 | 0.00 | 0.00 | 11 |
| **READY MIX CONCRETE** | | 30 | 0% | 0% | 08-Mar-26 | 14-Apr-26 | 09-Mar-26 A | 19-Mar-26 A | 0.00 | 0.00 | 0.00 | 19 |
| MLTX-02-005-EN | Pre-Qualification Submittal for Ready Mixed Concrete | 15 | 100% | 100% | 08-Mar-26 | 28-Mar-26 | 09-Mar-26 A | 11-Mar-26 A | 0.00 | 0.00 | 0.00 | 11 |
| MLTX-02-005-EN | Pre-Qualification Approval of Ready Mixed Concrete | 15 | 100% | 100% | 29-Mar-26 | 14-Apr-26 | 12-Mar-26 A | 19-Mar-26 A | 0.00 | 0.00 | 0.00 | 19 |
| **CONCRETE BLOCKS** | | 30 | 0% | 0% | 08-Mar-26 | 14-Apr-26 | 09-Mar-26 A | 19-Mar-26 A | 0.00 | 0.00 | 0.00 | 19 |
| MLTX-02-005-EN | Pre-Qualification Submittal for Concrete Blocks | 15 | 100% | 100% | 08-Mar-26 | 28-Mar-26 | 09-Mar-26 A | 11-Mar-26 A | 0.00 | 0.00 | 0.00 | 11 |
| MLTX-02-005-EN | Pre-Qualification Approval for Concrete Blocks | 15 | 100% | 100% | 29-Mar-26 | 14-Apr-26 | 12-Mar-26 A | 19-Mar-26 A | 0.00 | 0.00 | 0.00 | 19 |
| **WATER PROOFING** | | 36 | 0% | 0% | 08-Mar-26 | 21-Apr-26 | 09-Mar-26 A | 19-Mar-26 A | 0.00 | 0.00 | 0.00 | 25 |
| MLTX-02-005-EN | Pre-Qualification Submittal for Water Proofing | 15 | 100% | 100% | 08-Mar-26 | 28-Mar-26 | 09-Mar-26 A | 11-Mar-26 A | 0.00 | 0.00 | 0.00 | 11 |
| MLTX-02-005-EN | Pre-Qualification Approval for Water Proofing | 21 | 100% | 100% | 29-Mar-26 | 21-Apr-26 | 12-Mar-26 A | 19-Mar-26 A | 0.00 | 0.00 | 0.00 | 25 |
| **FLOOR/WALL TILES** | | 30 | 0% | 0% | 08-Mar-26 | 14-Apr-26 | 08-Mar-26 A | 10-May-26 A | 0.00 | 0.00 | 0.00 | -22 |
| MLTX-02-005-EN | Pre-Qualification Submittal for Tilling Materials | 15 | 100% | 100% | 08-Mar-26 | 28-Mar-26 | 08-Mar-26 A | 05-May-26 A | 0.00 | 0.00 | 0.00 | -33 |
| MLTX-02-005-EN | Pre-Qualification Approval for Tailling Material | 15 | 100% | 100% | 29-Mar-26 | 14-Apr-26 | 11-Mar-26 A | 10-May-26 A | 0.00 | 0.00 | 0.00 | -22 |
| **SUSPENDED CEILING** | | 30 | 0% | 0% | 08-Mar-26 | 14-Apr-26 | 09-Mar-26 A | 19-Mar-26 A | 0.00 | 0.00 | 0.00 | 19 |
| MLTX-02-005-EN | Pre-Qualification Submittal for Suspend Ceiling | 15 | 100% | 100% | 08-Mar-26 | 28-Mar-26 | 09-Mar-26 A | 11-Mar-26 A | 0.00 | 0.00 | 0.00 | 11 |
| MLTX-02-005-EN | Pre-Qualification Approval for Suspend Ceiling | 15 | 100% | 100% | 29-Mar-26 | 14-Apr-26 | 12-Mar-26 A | 19-Mar-26 A | 0.00 | 0.00 | 0.00 | 19 |
| **DOORS/WINDOWS** | | 30 | 0% | 0% | 08-Mar-26 | 14-Apr-26 | 09-Mar-26 A | 19-Mar-26 A | 0.00 | 0.00 | 0.00 | 19 |
| MLTX-02-005-EN | Pre-Qualification Submittal for Doors/Windows | 15 | 100% | 100% | 08-Mar-26 | 28-Mar-26 | 09-Mar-26 A | 11-Mar-26 A | 0.00 | 0.00 | 0.00 | 11 |
| MLTX-02-005-EN | Pre-Qualification Approval for Doors/Windows | 15 | 100% | 100% | 29-Mar-26 | 14-Apr-26 | 12-Mar-26 A | 19-Mar-26 A | 0.00 | 0.00 | 0.00 | 19 |
| **FURNITURES** | | 30 | 0% | 0% | 08-Mar-26 | 14-Apr-26 | 08-Mar-26 A | 10-May-26 A | 0.00 | 0.00 | 0.00 | -22 |
| MLTX-02-005-EN | Pre-Qualification Submittal for Furnitures | 15 | 100% | 100% | 08-Mar-26 | 28-Mar-26 | 08-Mar-26 A | 06-May-26 A | 0.00 | 0.00 | 0.00 | -34 |
| MLTX-02-005-EN | Pre-Qualification Approval for Furnitures | 15 | 100% | 100% | 29-Mar-26 | 14-Apr-26 | 11-Mar-26 A | 10-May-26 A | 0.00 | 0.00 | 0.00 | -22 |
| **SANITARY FIXTURES** | | 30 | 0% | 0% | 08-Mar-26 | 14-Apr-26 | 08-Mar-26 A | 10-May-26 A | 0.00 | 0.00 | 0.00 | -22 |
| MLTX-02-005-EN | Pre-Qualification Submittal for Sanitary Fixtures | 15 | 100% | 100% | 08-Mar-26 | 28-Mar-26 | 08-Mar-26 A | 06-May-26 A | 0.00 | 0.00 | 0.00 | -34 |
| MLTX-02-005-EN | Pre-Qualification Approval for Sanitary Fixtures | 15 | 100% | 100% | 29-Mar-26 | 14-Apr-26 | 11-Mar-26 A | 10-May-26 A | 0.00 | 0.00 | 0.00 | -22 |
| **WATER SUPPLY PIPES** | | 30 | 0% | 0% | 08-Mar-26 | 14-Apr-26 | 09-Mar-26 A | 19-Mar-26 A | 0.00 | 0.00 | 0.00 | 19 |
| MLTX-02-005-EN | Pre-Qualification Submittal for Water Supply Pipes | 15 | 100% | 100% | 08-Mar-26 | 28-Mar-26 | 09-Mar-26 A | 11-Mar-26 A | 0.00 | 0.00 | 0.00 | 11 |
| MLTX-02-005-EN | Pre-Qualification Approval for Water Supply Pipes | 15 | 100% | 100% | 29-Mar-26 | 14-Apr-26 | 12-Mar-26 A | 19-Mar-26 A | 0.00 | 0.00 | 0.00 | 19 |
| **SEWAGE/DRAINAGE PIPES** | | 30 | 0% | 0% | 08-Mar-26 | 14-Apr-26 | 09-Mar-26 A | 19-Mar-26 A | 0.00 | 0.00 | 0.00 | 19 |
| MLTX-02-005-EN | Pre-Qualification Submittal for Sewage/Drainage Pipes | 15 | 100% | 100% | 08-Mar-26 | 28-Mar-26 | 09-Mar-26 A | 11-Mar-26 A | 0.00 | 0.00 | 0.00 | 11 |
| MLTX-02-005-EN | Pre-Qualification Approval for Sewage/Drainage Pipes | 15 | 100% | 100% | 29-Mar-26 | 14-Apr-26 | 12-Mar-26 A | 19-Mar-26 A | 0.00 | 0.00 | 0.00 | 19 |
| **PACKAGE AC UNITS** | | 30 | 0% | 0% | 29-Mar-26 | 02-May-26 | 12-Mar-26 A | 24-Mar-26 A | 0.00 | 0.00 | 0.00 | 33 |
| MLTX-02-005-EN | Pre-Qualification Submittal for Package AC Units | 15 | 100% | 100% | 29-Mar-26 | 14-Apr-26 | 12-Mar-26 A | 15-Mar-26 A | 0.00 | 0.00 | 0.00 | 23 |
| MLTX-02-005-EN | Pre-Qualification Approval for Package AC Units | 15 | 100% | 100% | 15-Apr-26 | 02-May-26 | 16-Mar-26 A | 24-Mar-26 A | 0.00 | 0.00 | 0.00 | 33 |
| **AIR DIFUSSERS/GRILLS** | | 30 | 0% | 0% | 29-Mar-26 | 02-May-26 | 12-Mar-26 A | 06-May-26 A | 0.00 | 0.00 | 0.00 | -3 |

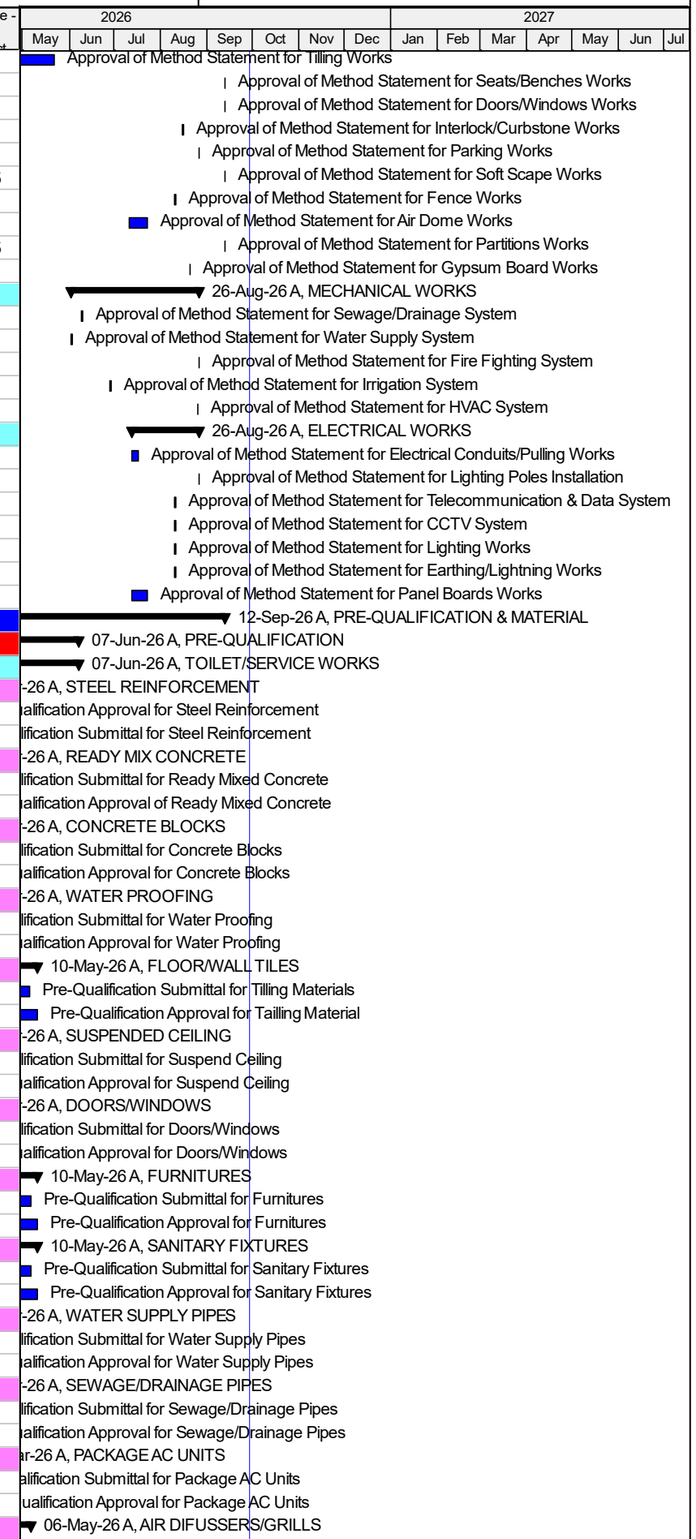


Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary




TASK filter: All Activities

© Oracle Corporation

# MLTX-02-005 - Playground Initiative for Eastern Region (Arar-Hasa osis -Dammam)

**Updateded schedule**
**D.D 28-09-2026**

| Activity ID | Activity Name | Original Duration | Schedule % Complete | Performance % Complete | BL Project Start | BL Project Finish | Start | Finish | Planned Value Cost | Earned Value Cost | Budgeted Total Cost | Variance - BL Project |
|---|---|---|---|---|---|---|---|---|---|---|---|---|
| MLTX-02-005-EN | Pre-Qualification Submittal for Air Diffusers/Grills | 15 | 100% | 100% | 29-Mar-26 | 14-Apr-26 | 12-Mar-26 A | 06-May-26 A | 0.00 | 0.00 | 0.00 | -18 |
| MLTX-02-005-EN | Pre-Qualification Approval for Air Diffusers/Grills | 15 | 100% | 100% | 15-Apr-26 | 02-May-26 | 16-Mar-26 A | 06-May-26 A | 0.00 | 0.00 | 0.00 | -3 |
| **GALVANIZED DUCTS** | | 30 | 0% | 0% | 29-Mar-26 | 02-May-26 | 11-Mar-26 A | 30-Apr-26 A | 0.00 | 0.00 | 0.00 | 1 |
| MLTX-02-005-EN | Pre-Qualification Submittal for Galvanized Ducts | 15 | 100% | 100% | 29-Mar-26 | 14-Apr-26 | 11-Mar-26 A | 25-Apr-26 A | 0.00 | 0.00 | 0.00 | -9 |
| MLTX-02-005-EN | Pre-Qualification Approval for Galvanized Ducts | 15 | 100% | 100% | 15-Apr-26 | 02-May-26 | 15-Mar-26 A | 30-Apr-26 A | 0.00 | 0.00 | 0.00 | 1 |
| **EXHAUST FANS** | | 30 | 0% | 0% | 29-Mar-26 | 02-May-26 | 11-Mar-26 A | 07-Jun-26 A | 0.00 | 0.00 | 0.00 | -28 |
| MLTX-02-005-EN | Pre-Qualification Submittal for Exhaust Fans | 15 | 100% | 100% | 29-Mar-26 | 14-Apr-26 | 11-Mar-26 A | 25-May-26 A | 0.00 | 0.00 | 0.00 | -35 |
| MLTX-02-005-EN | Pre-Qualification Approval for Exhaust Fans | 15 | 100% | 100% | 15-Apr-26 | 02-May-26 | 15-Mar-26 A | 07-Jun-26 A | 0.00 | 0.00 | 0.00 | -28 |
| **LIGHTING FIXTURES** | | 30 | 0% | 0% | 29-Mar-26 | 02-May-26 | 11-Mar-26 A | 07-Jun-26 A | 0.00 | 0.00 | 0.00 | -28 |
| MLTX-02-005-EN | Pre-Qualification Submittal for Lighting Fixtures | 15 | 100% | 100% | 29-Mar-26 | 14-Apr-26 | 11-Mar-26 A | 25-May-26 A | 0.00 | 0.00 | 0.00 | -35 |
| MLTX-02-005-EN | Pre-Qualification Approval for Lighting Fixtures | 15 | 100% | 100% | 15-Apr-26 | 02-May-26 | 15-Mar-26 A | 07-Jun-26 A | 0.00 | 0.00 | 0.00 | -28 |
| **SWITCHES/SOCKETS** | | 30 | 0% | 0% | 29-Mar-26 | 02-May-26 | 11-Mar-26 A | 07-Jun-26 A | 0.00 | 0.00 | 0.00 | -28 |
| MLTX-02-005-EN | Pre-Qualification Submittal for Switches/Sockets | 15 | 100% | 100% | 29-Mar-26 | 14-Apr-26 | 11-Mar-26 A | 25-May-26 A | 0.00 | 0.00 | 0.00 | -35 |
| MLTX-02-005-EN | Pre-Qualification Approval for Switches/Sockets | 15 | 100% | 100% | 15-Apr-26 | 02-May-26 | 15-Mar-26 A | 07-Jun-26 A | 0.00 | 0.00 | 0.00 | -28 |
| **EARTHING SYSTEM** | | 30 | 0% | 0% | 29-Mar-26 | 02-May-26 | 11-Mar-26 A | 11-May-26 A | 0.00 | 0.00 | 0.00 | -8 |
| MLTX-02-005-EN | Pre-Qualification Submittal for Earthing System | 15 | 100% | 100% | 29-Mar-26 | 14-Apr-26 | 11-Mar-26 A | 09-May-26 A | 0.00 | 0.00 | 0.00 | -21 |
| MLTX-02-005-EN | Pre-Qualification Approval for Earthing System | 15 | 100% | 100% | 15-Apr-26 | 02-May-26 | 15-Mar-26 A | 11-May-26 A | 0.00 | 0.00 | 0.00 | -8 |
| **DISTRIBUTION PANNELS** | | 30 | 0% | 0% | 29-Mar-26 | 02-May-26 | 11-Mar-26 A | 07-Jun-26 A | 0.00 | 0.00 | 0.00 | -28 |
| MLTX-02-005-EN | Pre-Qualification Submittal for Distribution Panels | 15 | 100% | 100% | 29-Mar-26 | 14-Apr-26 | 11-Mar-26 A | 25-May-26 A | 0.00 | 0.00 | 0.00 | -35 |
| MLTX-02-005-EN | Pre-Qualification Approval for Distribution Panels | 15 | 100% | 100% | 15-Apr-26 | 02-May-26 | 15-Mar-26 A | 07-Jun-26 A | 0.00 | 0.00 | 0.00 | -28 |
| **PLAYGROUND WORKS** | | 45 | 0% | 0% | 08-Mar-26 | 02-May-26 | 08-Mar-26 A | 07-Jun-26 A | 0.00 | 0.00 | 0.00 | -28 |
| **PVC MEMBRANE** | | 30 | 0% | 0% | 08-Mar-26 | 14-Apr-26 | 08-Mar-26 A | 24-May-26 A | 0.00 | 0.00 | 0.00 | -34 |
| MLTX-02-005-EN | Pre-Qualification Submittal for PVC Membrane | 15 | 100% | 100% | 08-Mar-26 | 28-Mar-26 | 08-Mar-26 A | 20-May-26 A | 0.00 | 0.00 | 0.00 | -46 |
| MLTX-02-005-EN | Pre-Qualification Approval for PVC Membrane | 15 | 100% | 100% | 29-Mar-26 | 14-Apr-26 | 11-Mar-26 A | 24-May-26 A | 0.00 | 0.00 | 0.00 | -34 |
| **STEEL TENSION CABLES** | | 30 | 0% | 0% | 08-Mar-26 | 14-Apr-26 | 08-Mar-26 A | 24-May-26 A | 0.00 | 0.00 | 0.00 | -34 |
| MLTX-02-005-EN | Pre-Qualification Submittal for Steel Tension Cables | 15 | 100% | 100% | 08-Mar-26 | 28-Mar-26 | 08-Mar-26 A | 20-May-26 A | 0.00 | 0.00 | 0.00 | -46 |
| MLTX-02-005-EN | Pre-Qualification Approval for Steel Tension Cables | 15 | 100% | 100% | 29-Mar-26 | 14-Apr-26 | 11-Mar-26 A | 24-May-26 A | 0.00 | 0.00 | 0.00 | -34 |
| **EMERGENCY DOORS** | | 30 | 0% | 0% | 08-Mar-26 | 14-Apr-26 | 08-Mar-26 A | 24-May-26 A | 0.00 | 0.00 | 0.00 | -34 |
| MLTX-02-005-EN | Pre-Qualification Submittal for Emergency Doors | 15 | 100% | 100% | 08-Mar-26 | 28-Mar-26 | 08-Mar-26 A | 20-May-26 A | 0.00 | 0.00 | 0.00 | -46 |
| MLTX-02-005-EN | Pre-Qualification Approval for Emergency Doors | 15 | 100% | 100% | 29-Mar-26 | 14-Apr-26 | 11-Mar-26 A | 24-May-26 A | 0.00 | 0.00 | 0.00 | -34 |
| **PRESSURE UNITS** | | 30 | 0% | 0% | 08-Mar-26 | 14-Apr-26 | 08-Mar-26 A | 24-May-26 A | 0.00 | 0.00 | 0.00 | -34 |
| MLTX-02-005-EN | Pre-Qualification Submittal for Pressure Units | 15 | 100% | 100% | 08-Mar-26 | 28-Mar-26 | 08-Mar-26 A | 20-May-26 A | 0.00 | 0.00 | 0.00 | -46 |
| MLTX-02-005-EN | Pre-Qualification Approval for Pressure Units | 15 | 100% | 100% | 29-Mar-26 | 14-Apr-26 | 11-Mar-26 A | 24-May-26 A | 0.00 | 0.00 | 0.00 | -34 |
| **AIR LOCK DOORS** | | 30 | 0% | 0% | 08-Mar-26 | 14-Apr-26 | 08-Mar-26 A | 24-May-26 A | 0.00 | 0.00 | 0.00 | -34 |
| MLTX-02-005-EN | Pre-Qualification Submittal for Lock Doors | 15 | 100% | 100% | 08-Mar-26 | 28-Mar-26 | 08-Mar-26 A | 20-May-26 A | 0.00 | 0.00 | 0.00 | -46 |
| MLTX-02-005-EN | Pre-Qualification Approval for Lock Doors | 15 | 100% | 100% | 29-Mar-26 | 14-Apr-26 | 11-Mar-26 A | 24-May-26 A | 0.00 | 0.00 | 0.00 | -34 |
| **ARTIFICIAL TURF** | | 30 | 0% | 0% | 08-Mar-26 | 14-Apr-26 | 08-Mar-26 A | 10-May-26 A | 0.00 | 0.00 | 0.00 | -22 |
| MLTX-02-005-EN | Pre-Qualification Submittal for Artificial TURF | 15 | 100% | 100% | 08-Mar-26 | 28-Mar-26 | 08-Mar-26 A | 06-May-26 A | 0.00 | 0.00 | 0.00 | -34 |
| MLTX-02-005-EN | Pre-Qualification Approval for Artificial TURF | 15 | 100% | 100% | 29-Mar-26 | 14-Apr-26 | 11-Mar-26 A | 10-May-26 A | 0.00 | 0.00 | 0.00 | -22 |
| **RUBBER GRANULES** | | 36 | 0% | 0% | 08-Mar-26 | 21-Apr-26 | 08-Mar-26 A | 10-May-26 A | 0.00 | 0.00 | 0.00 | -16 |
| MLTX-02-005-EN | Pre-Qualification Submittal for Rubber Granules | 15 | 100% | 100% | 08-Mar-26 | 28-Mar-26 | 08-Mar-26 A | 06-May-26 A | 0.00 | 0.00 | 0.00 | -34 |
| MLTX-02-005-EN | Pre-Qualification Approval for Rubber Granules | 21 | 100% | 100% | 29-Mar-26 | 21-Apr-26 | 11-Mar-26 A | 10-May-26 A | 0.00 | 0.00 | 0.00 | -16 |
| **PADEL GLASS** | | 30 | 0% | 0% | 08-Mar-26 | 14-Apr-26 | 08-Mar-26 A | 10-May-26 A | 0.00 | 0.00 | 0.00 | -22 |
| MLTX-02-005-EN | Pre-Qualification Submittal for Padel Glass | 15 | 100% | 100% | 08-Mar-26 | 28-Mar-26 | 08-Mar-26 A | 06-May-26 A | 0.00 | 0.00 | 0.00 | -34 |
| MLTX-02-005-EN | Pre-Qualification Approval for Padel Glass | 15 | 100% | 100% | 29-Mar-26 | 14-Apr-26 | 11-Mar-26 A | 10-May-26 A | 0.00 | 0.00 | 0.00 | -22 |
| **PADEL WIRE MESH/STEEL SETS** | | 30 | 0% | 0% | 08-Mar-26 | 14-Apr-26 | 08-Mar-26 A | 10-May-26 A | 0.00 | 0.00 | 0.00 | -22 |
| MLTX-02-005-EN | Pre-Qualification Submittal for Wire Mesh/Steel Sets | 15 | 100% | 100% | 08-Mar-26 | 28-Mar-26 | 08-Mar-26 A | 06-May-26 A | 0.00 | 0.00 | 0.00 | -34 |
| MLTX-02-005-EN | Pre-Qualification Approval for Wire Mesh/Steel Sets | 15 | 100% | 100% | 29-Mar-26 | 14-Apr-26 | 11-Mar-26 A | 10-May-26 A | 0.00 | 0.00 | 0.00 | -22 |
| **AGGREGATE BASE COURSE** | | 36 | 0% | 0% | 08-Mar-26 | 21-Apr-26 | 08-Mar-26 A | 30-Apr-26 A | 0.00 | 0.00 | 0.00 | -8 |
| MLTX-02-005-EN | Pre-Qualification Submittal for Aggregate Base Course | 15 | 100% | 100% | 08-Mar-26 | 28-Mar-26 | 08-Mar-26 A | 26-Apr-26 A | 0.00 | 0.00 | 0.00 | -25 |
| MLTX-02-005-EN | Pre-Qualification Approval for Aggregate Base Course | 21 | 100% | 100% | 29-Mar-26 | 21-Apr-26 | 11-Mar-26 A | 30-Apr-26 A | 0.00 | 0.00 | 0.00 | -8 |
| **BITUMINOUS BASE & WEARING COURSE** | | 30 | 0% | 0% | 29-Mar-26 | 02-May-26 | 11-Mar-26 A | 30-Apr-26 A | 0.00 | 0.00 | 0.00 | 1 |
| MLTX-02-005-EN | Pre-Qualification Submittal for Bituminous Base & Wearing | 15 | 100% | 100% | 29-Mar-26 | 14-Apr-26 | 11-Mar-26 A | 26-Apr-26 A | 0.00 | 0.00 | 0.00 | -10 |
| MLTX-02-005-EN | Pre-Qualification Approval for the Site | 15 | 100% | 100% | 15-Apr-26 | 02-May-26 | 15-Mar-26 A | 30-Apr-26 A | 0.00 | 0.00 | 0.00 | 1 |
| **INTERLOCKING PAVING** | | 30 | 0% | 0% | 29-Mar-26 | 02-May-26 | 11-Mar-26 A | 14-Apr-26 A | 0.00 | 0.00 | 0.00 | 15 |
| MLTX-02-005-EN | Pre-Qualification Submittal for Interlocking Block Pavers | 15 | 100% | 100% | 29-Mar-26 | 14-Apr-26 | 11-Mar-26 A | 11-Apr-26 A | 0.00 | 0.00 | 0.00 | 3 |
| MLTX-02-005-EN | Pre-Qualification Approval for Interlocking Block Pavers | 15 | 100% | 100% | 15-Apr-26 | 02-May-26 | 15-Mar-26 A | 14-Apr-26 A | 0.00 | 0.00 | 0.00 | 15 |
| **MARKING PAINT** | | 30 | 0% | 0% | 29-Mar-26 | 02-May-26 | 11-Mar-26 A | 09-May-26 A | 0.00 | 0.00 | 0.00 | -6 |
| MLTX-02-005-EN | Pre-Qualification Submittal for Marking Paint | 15 | 100% | 100% | 29-Mar-26 | 14-Apr-26 | 11-Mar-26 A | 05-May-26 A | 0.00 | 0.00 | 0.00 | -18 |
| MLTX-02-005-EN | Pre-Qualification Approval for Marking Paint | 15 | 100% | 100% | 15-Apr-26 | 02-May-26 | 15-Mar-26 A | 09-May-26 A | 0.00 | 0.00 | 0.00 | -6 |
| **PACKAGE AC UNITS** | | 30 | 0% | 0% | 29-Mar-26 | 02-May-26 | 11-Mar-26 A | 07-Jun-26 A | 0.00 | 0.00 | 0.00 | -28 |
| MLTX-02-005-EN | Pre-Qualification Submittal for Package AC Units | 15 | 100% | 100% | 29-Mar-26 | 14-Apr-26 | 11-Mar-26 A | 25-May-26 A | 0.00 | 0.00 | 0.00 | -35 |
| MLTX-02-005-EN | Pre-Qualification Approval for Package AC Units | 15 | 100% | 100% | 15-Apr-26 | 02-May-26 | 15-Mar-26 A | 07-Jun-26 A | 0.00 | 0.00 | 0.00 | -28 |
| **AIR DIFUSSERS/GRILLS** | | 30 | 0% | 0% | 29-Mar-26 | 02-May-26 | 11-Mar-26 A | 07-Jun-26 A | 0.00 | 0.00 | 0.00 | -28 |

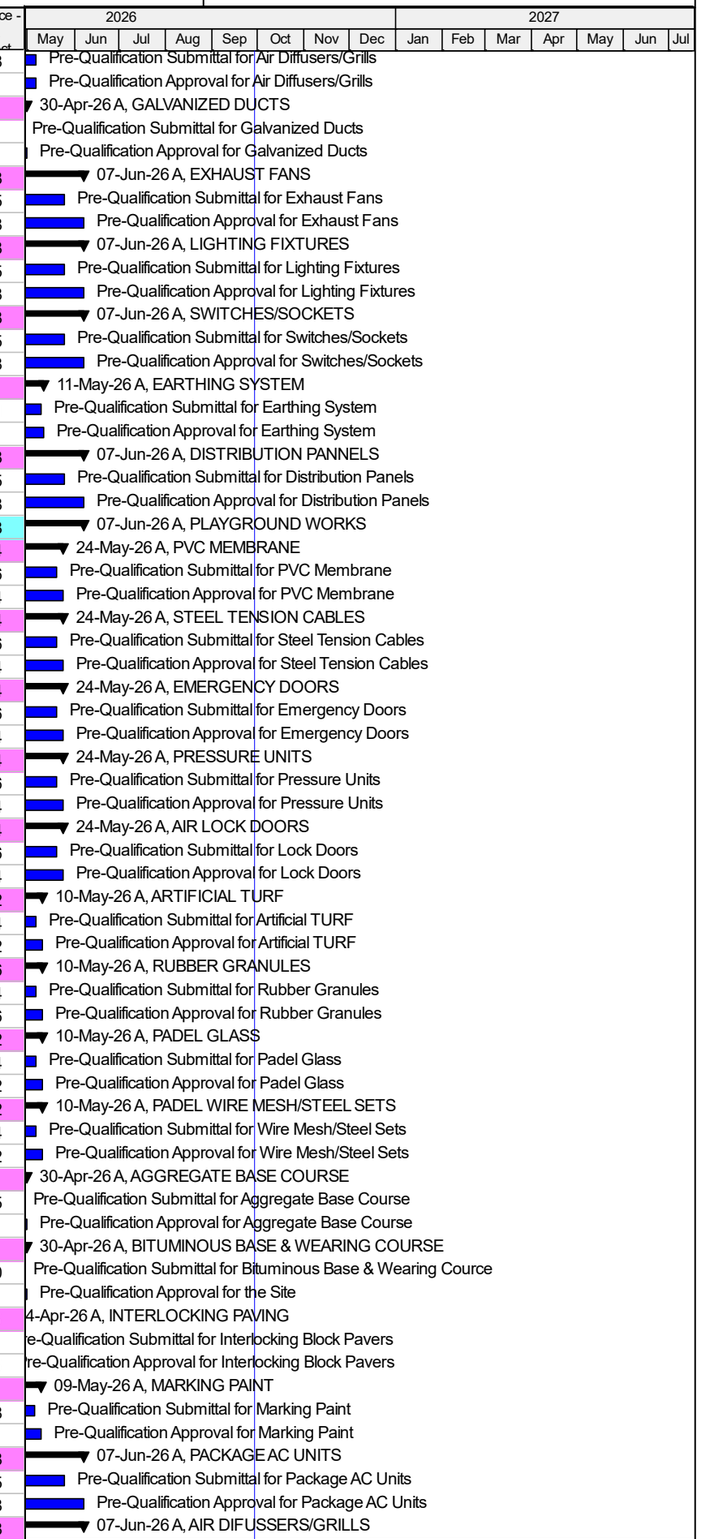


Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary




TASK filter: All Activities

© Oracle Corporation

# MLTX-02-005 - Playground Initiative for Eastern Region (Arar-Hasa osis -Dammam)

**Updateded schedule**
**D.D 28-09-2026**

| Activity ID | Activity Name | Original Duration | Schedule % Complete | Performance % Complete | BL Project Start | BL Project Finish | Start | Finish | Planned Value Cost | Earned Value Cost | Budgeted Total Cost | Variance - BL Project |
|---|---|---|---|---|---|---|---|---|---|---|---|---|
| MLTX-02-005-EN | Pre-Qualification Submittal for Air Difussers/Grills | 15 | 100% | 100% | 29-Mar-26 | 14-Apr-26 | 11-Mar-26 A | 25-May-26 A | 0.00 | 0.00 | 0.00 | -35 |
| MLTX-02-005-EN | Pre-Qualification Approval for Air Difussers/Grills | 15 | 100% | 100% | 15-Apr-26 | 02-May-26 | 15-Mar-26 A | 07-Jun-26 A | 0.00 | 0.00 | 0.00 | -28 |
| **GALVANIZED DUCTS** | | 30 | 0% | 0% | 29-Mar-26 | 02-May-26 | 11-Mar-26 A | 30-Apr-26 A | 0.00 | 0.00 | 0.00 | 1 |
| MLTX-02-005-EN | Pre-Qualification Submittal for Galvanized Duct | 15 | 100% | 100% | 29-Mar-26 | 14-Apr-26 | 11-Mar-26 A | 30-Apr-26 A | 0.00 | 0.00 | 0.00 | -14 |
| MLTX-02-005-EN | Pre-Qualification Approval for Galvanized Duct | 15 | 100% | 100% | 15-Apr-26 | 02-May-26 | 15-Mar-26 A | 25-Apr-26 A | 0.00 | 0.00 | 0.00 | 6 |
| **EXHAUST FANS** | | 30 | 0% | 0% | 29-Mar-26 | 02-May-26 | 11-Mar-26 A | 07-Jun-26 A | 0.00 | 0.00 | 0.00 | -28 |
| MLTX-02-005-EN | Pre-Qualification Submittal for Exhaust Fans | 15 | 100% | 100% | 29-Mar-26 | 14-Apr-26 | 11-Mar-26 A | 25-May-26 A | 0.00 | 0.00 | 0.00 | -35 |
| MLTX-02-005-EN | Pre-Qualification Approval for Exhaust Fans | 15 | 100% | 100% | 15-Apr-26 | 02-May-26 | 15-Mar-26 A | 07-Jun-26 A | 0.00 | 0.00 | 0.00 | -28 |
| **DISTRIBUTION BOARDS** | | 30 | 0% | 0% | 29-Mar-26 | 02-May-26 | 11-Mar-26 A | 07-Jun-26 A | 0.00 | 0.00 | 0.00 | -28 |
| MLTX-02-005-EN | Pre-Qualification Submittal for Distribution Boards | 15 | 100% | 100% | 29-Mar-26 | 14-Apr-26 | 11-Mar-26 A | 25-May-26 A | 0.00 | 0.00 | 0.00 | -35 |
| MLTX-02-005-EN | Pre-Qualification Approval for Distribution Boards | 15 | 100% | 100% | 15-Apr-26 | 02-May-26 | 15-Mar-26 A | 07-Jun-26 A | 0.00 | 0.00 | 0.00 | -28 |
| **POWER CABLES** | | 30 | 0% | 0% | 29-Mar-26 | 02-May-26 | 11-Mar-26 A | 11-May-26 A | 0.00 | 0.00 | 0.00 | -8 |
| MLTX-02-005-EN | Pre-Qualification Submittal for Power Cables | 15 | 100% | 100% | 29-Mar-26 | 14-Apr-26 | 11-Mar-26 A | 09-May-26 A | 0.00 | 0.00 | 0.00 | -21 |
| MLTX-02-005-EN | Pre-Qualification Approval for Power Cables | 15 | 100% | 100% | 15-Apr-26 | 02-May-26 | 15-Mar-26 A | 11-May-26 A | 0.00 | 0.00 | 0.00 | -8 |
| **LIGHT FIXTURES** | | 30 | 0% | 0% | 29-Mar-26 | 02-May-26 | 11-Mar-26 A | 07-Jun-26 A | 0.00 | 0.00 | 0.00 | -28 |
| MLTX-02-005-EN | Pre-Qualification Submittal for Light Fixtures | 15 | 100% | 100% | 29-Mar-26 | 14-Apr-26 | 11-Mar-26 A | 25-May-26 A | 0.00 | 0.00 | 0.00 | -35 |
| MLTX-02-005-EN | Pre-Qualification Approval for Light Fixtures | 15 | 100% | 100% | 15-Apr-26 | 02-May-26 | 15-Mar-26 A | 07-Jun-26 A | 0.00 | 0.00 | 0.00 | -28 |
| **CCTV MATERIALS** | | 30 | 0% | 0% | 29-Mar-26 | 02-May-26 | 11-Mar-26 A | 07-Jun-26 A | 0.00 | 0.00 | 0.00 | -28 |
| MLTX-02-005-EN | Pre-Qualification Submittal for CCTV | 15 | 100% | 100% | 29-Mar-26 | 14-Apr-26 | 11-Mar-26 A | 25-May-26 A | 0.00 | 0.00 | 0.00 | -35 |
| MLTX-02-005-EN | Pre-Qualification Approval for CCTV | 15 | 100% | 100% | 15-Apr-26 | 02-May-26 | 15-Mar-26 A | 07-Jun-26 A | 0.00 | 0.00 | 0.00 | -28 |
| **POWER OUTLETS/SWITCHES** | | 30 | 0% | 0% | 29-Mar-26 | 02-May-26 | 11-Mar-26 A | 07-Jun-26 A | 0.00 | 0.00 | 0.00 | -28 |
| MLTX-02-005-EN | Pre-Qualification Submittal for Power Outlets/Switches | 15 | 100% | 100% | 29-Mar-26 | 14-Apr-26 | 11-Mar-26 A | 25-May-26 A | 0.00 | 0.00 | 0.00 | -35 |
| MLTX-02-005-EN | Pre-Qualification Approval for Power Outlets/Switches | 15 | 100% | 100% | 15-Apr-26 | 02-May-26 | 15-Mar-26 A | 07-Jun-26 A | 0.00 | 0.00 | 0.00 | -28 |
| **LANDSCAPE WORKS** | | 30 | 0% | 0% | 29-Mar-26 | 02-May-26 | 11-Mar-26 A | 18-May-26 A | 0.00 | 0.00 | 0.00 | -14 |
| **INTERLOCKING PAVING** | | 30 | 0% | 0% | 29-Mar-26 | 02-May-26 | 12-Mar-26 A | 24-Mar-26 A | 0.00 | 0.00 | 0.00 | 33 |
| MLTX-02-005-EN | Pre-Qualification Submittal for Interlocking Block Pavers | 15 | 100% | 100% | 29-Mar-26 | 14-Apr-26 | 12-Mar-26 A | 15-Mar-26 A | 0.00 | 0.00 | 0.00 | 23 |
| MLTX-02-005-EN | Pre-Qualification Approval for Interlocking Block Pavers | 15 | 100% | 100% | 15-Apr-26 | 02-May-26 | 16-Mar-26 A | 24-Mar-26 A | 0.00 | 0.00 | 0.00 | 33 |
| **CURBSTONE** | | 30 | 0% | 0% | 29-Mar-26 | 02-May-26 | 12-Mar-26 A | 24-Mar-26 A | 0.00 | 0.00 | 0.00 | 33 |
| MLTX-02-005-EN | Pre-Qualification Submittal for Curbstone | 15 | 100% | 100% | 29-Mar-26 | 14-Apr-26 | 12-Mar-26 A | 15-Mar-26 A | 0.00 | 0.00 | 0.00 | 23 |
| MLTX-02-005-EN | Pre-Qualification Approval for Curbstone | 15 | 100% | 100% | 15-Apr-26 | 02-May-26 | 16-Mar-26 A | 24-Mar-26 A | 0.00 | 0.00 | 0.00 | 33 |
| **PAVEMENT MARKING** | | 30 | 0% | 0% | 29-Mar-26 | 02-May-26 | 11-Mar-26 A | 09-May-26 A | 0.00 | 0.00 | 0.00 | -6 |
| MLTX-02-005-EN | Pre-Qualification Submittal for Pavement Markings | 15 | 100% | 100% | 29-Mar-26 | 14-Apr-26 | 11-Mar-26 A | 05-May-26 A | 0.00 | 0.00 | 0.00 | -18 |
| MLTX-02-005-EN | Pre-Qualification Approval for Pavement Markings | 15 | 100% | 100% | 15-Apr-26 | 02-May-26 | 15-Mar-26 A | 09-May-26 A | 0.00 | 0.00 | 0.00 | -6 |
| **TRAFFIC SIGNS** | | 30 | 0% | 0% | 29-Mar-26 | 02-May-26 | 11-Mar-26 A | 09-May-26 A | 0.00 | 0.00 | 0.00 | -6 |
| MLTX-02-005-EN | Pre-Qualification Submittal for Traffic Signs | 15 | 100% | 100% | 29-Mar-26 | 14-Apr-26 | 11-Mar-26 A | 05-May-26 A | 0.00 | 0.00 | 0.00 | -18 |
| MLTX-02-005-EN | Pre-Qualification Approval for Traffic Signs | 15 | 100% | 100% | 15-Apr-26 | 02-May-26 | 15-Mar-26 A | 09-May-26 A | 0.00 | 0.00 | 0.00 | -6 |
| **IRRIGATION PIPES/SPRINKLERS** | | 30 | 0% | 0% | 29-Mar-26 | 02-May-26 | 11-Mar-26 A | 10-May-26 A | 0.00 | 0.00 | 0.00 | -7 |
| MLTX-02-005-EN | Pre-Qualification Submittal for Irrigation Pipes/Sprinkles | 15 | 100% | 100% | 29-Mar-26 | 14-Apr-26 | 11-Mar-26 A | 06-May-26 A | 0.00 | 0.00 | 0.00 | -19 |
| MLTX-02-005-EN | Pre-Qualification Approval for Irrigation Pipes/Sprinkles | 15 | 100% | 100% | 15-Apr-26 | 02-May-26 | 15-Mar-26 A | 10-May-26 A | 0.00 | 0.00 | 0.00 | -7 |
| **AGRICULTURE SOIL** | | 30 | 0% | 0% | 29-Mar-26 | 02-May-26 | 11-Mar-26 A | 14-May-26 A | 0.00 | 0.00 | 0.00 | -10 |
| MLTX-02-005-EN | Pre-Qualification Submittal for Agriculture Soil | 15 | 100% | 100% | 29-Mar-26 | 14-Apr-26 | 11-Mar-26 A | 07-May-26 A | 0.00 | 0.00 | 0.00 | -20 |
| MLTX-02-005-EN | Pre-Qualification Approval for Agriculture Soil | 15 | 100% | 100% | 15-Apr-26 | 02-May-26 | 15-Mar-26 A | 14-May-26 A | 0.00 | 0.00 | 0.00 | -10 |
| **TRACK SURFACE** | | 30 | 0% | 0% | 29-Mar-26 | 02-May-26 | 11-Mar-26 A | 13-May-26 A | 0.00 | 0.00 | 0.00 | -10 |
| MLTX-02-005-EN | Pre-Qualification Submittal for Track Surface | 15 | 100% | 100% | 29-Mar-26 | 14-Apr-26 | 11-Mar-26 A | 10-May-26 A | 0.00 | 0.00 | 0.00 | -22 |
| MLTX-02-005-EN | Pre-Qualification Approval for Track Surface | 15 | 100% | 100% | 15-Apr-26 | 02-May-26 | 15-Mar-26 A | 13-May-26 A | 0.00 | 0.00 | 0.00 | -10 |
| **GRASS/TREES** | | 30 | 0% | 0% | 29-Mar-26 | 02-May-26 | 11-Mar-26 A | 18-May-26 A | 0.00 | 0.00 | 0.00 | -14 |
| MLTX-02-005-EN | Pre-Qualification Submittal for Grass/Trees | 15 | 100% | 100% | 29-Mar-26 | 14-Apr-26 | 11-Mar-26 A | 13-May-26 A | 0.00 | 0.00 | 0.00 | -25 |
| MLTX-02-005-EN | Pre-Qualification Approval for Grass/Trees | 15 | 100% | 100% | 15-Apr-26 | 02-May-26 | 15-Mar-26 A | 18-May-26 A | 0.00 | 0.00 | 0.00 | -14 |
| **CABLES** | | 30 | 0% | 0% | 29-Mar-26 | 02-May-26 | 11-Mar-26 A | 11-May-26 A | 0.00 | 0.00 | 0.00 | -8 |
| MLTX-02-005-EN | Pre-Qualification Submittal for Cables | 15 | 100% | 100% | 29-Mar-26 | 14-Apr-26 | 11-Mar-26 A | 09-May-26 A | 0.00 | 0.00 | 0.00 | -21 |
| MLTX-02-005-EN | Pre-Qualification Approval for Cables | 15 | 100% | 100% | 15-Apr-26 | 02-May-26 | 15-Mar-26 A | 11-May-26 A | 0.00 | 0.00 | 0.00 | -8 |
| **LIGHT POLES** | | 30 | 0% | 0% | 29-Mar-26 | 02-May-26 | 11-Mar-26 A | 04-May-26 A | 0.00 | 0.00 | 0.00 | -2 |
| MLTX-02-005-EN | Pre-Qualification Submittal for Lighting poles | 15 | 100% | 100% | 29-Mar-26 | 14-Apr-26 | 11-Mar-26 A | 30-Apr-26 A | 0.00 | 0.00 | 0.00 | -14 |
| MLTX-02-005-EN | Pre-Qualification Approval for Lighting poles | 15 | 100% | 100% | 15-Apr-26 | 02-May-26 | 15-Mar-26 A | 04-May-26 A | 0.00 | 0.00 | 0.00 | -2 |
| **MATERIAL SUBMITTAL** | | 84 | 0% | 0% | 15-Apr-26 | 13-Jun-26 | 19-Mar-26 A | 12-Sep-26 A | 0.00 | 0.00 | 0.00 | -78 |
| **TOILET/SERVICE WORKS** | | 65 | 0% | 0% | 15-Apr-26 | 09-Jun-26 | 19-Mar-26 A | 30-Jul-26 A | 0.00 | 0.00 | 0.00 | -44 |
| **STEEL REINFORCEMENT** | | 30 | 0% | 0% | 15-Apr-26 | 19-May-26 | 24-Mar-26 A | 04-Apr-26 A | 0.00 | 0.00 | 0.00 | 39 |
| MLTX-02-005-EN | Material Submittal for Steel Reinforcement | 15 | 100% | 100% | 15-Apr-26 | 02-May-26 | 24-Mar-26 A | 26-Mar-26 A | 0.00 | 0.00 | 0.00 | 31 |
| MLTX-02-005-EN | Material Approval for Steel Reinforcement | 15 | 100% | 100% | 03-May-26 | 19-May-26 | 28-Mar-26 A | 04-Apr-26 A | 0.00 | 0.00 | 0.00 | 39 |
| **READY MIX CONCRETE** | | 30 | 0% | 0% | 15-Apr-26 | 19-May-26 | 24-Mar-26 A | 04-Apr-26 A | 0.00 | 0.00 | 0.00 | 39 |
| MLTX-02-005-EN | Material Submittal for Ready Mixed Concrete | 15 | 100% | 100% | 15-Apr-26 | 02-May-26 | 24-Mar-26 A | 26-Mar-26 A | 0.00 | 0.00 | 0.00 | 31 |
| MLTX-02-005-EN | Material Approval of Ready Mixed Concrete | 15 | 100% | 100% | 03-May-26 | 19-May-26 | 28-Mar-26 A | 04-Apr-26 A | 0.00 | 0.00 | 0.00 | 39 |
| **CONCRETE BLOCKS** | | 30 | 0% | 0% | 15-Apr-26 | 19-May-26 | 24-Mar-26 A | 04-Apr-26 A | 0.00 | 0.00 | 0.00 | 39 |
| MLTX-02-005-EN | Material Submittal for Concrete Blocks | 15 | 100% | 100% | 15-Apr-26 | 02-May-26 | 24-Mar-26 A | 26-Mar-26 A | 0.00 | 0.00 | 0.00 | 31 |

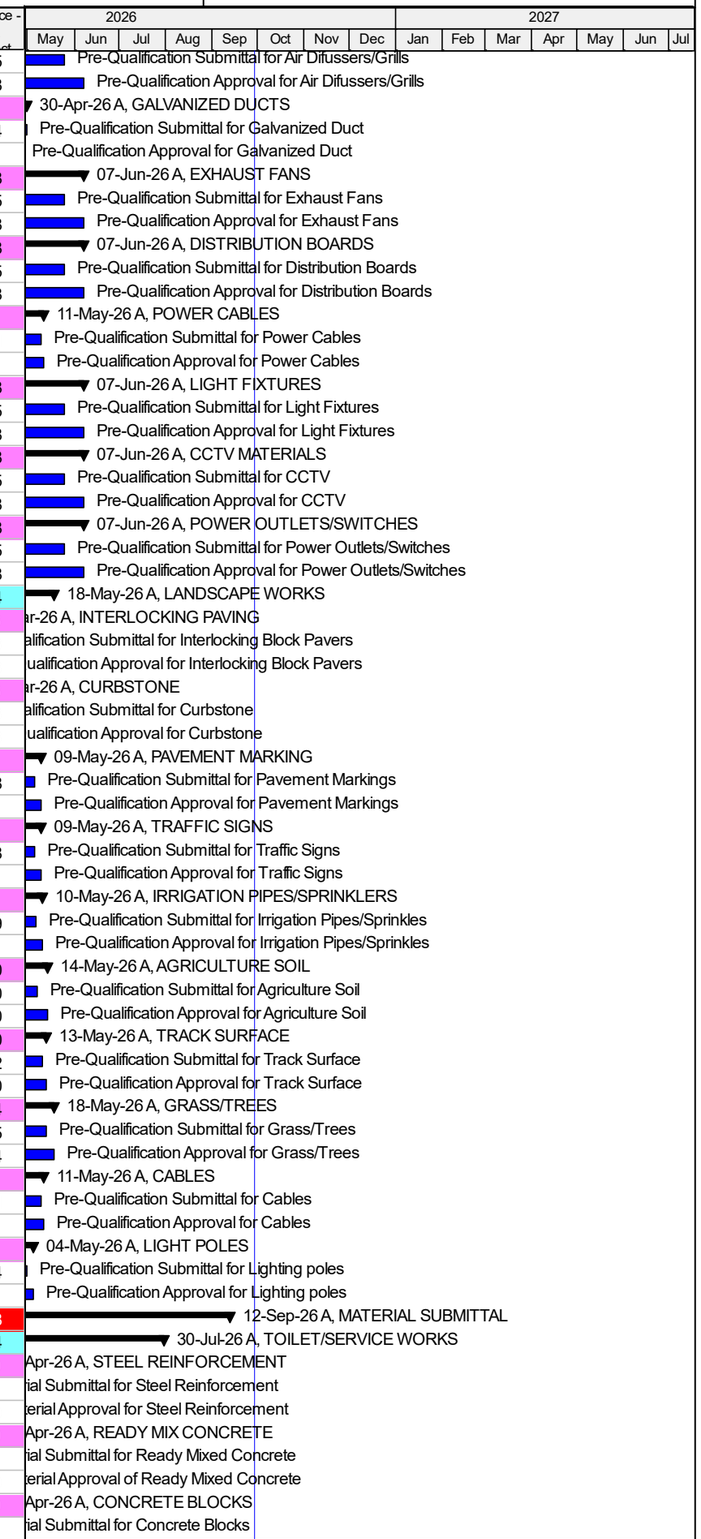


Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary




TASK filter: All Activities

© Oracle Corporation

# MLTX-02-005 - Playground Initiative for Eastern Region (Arar-Hasa osis -Dammam)

**Updateded schedule**
**D.D 28-09-2026**

| Activity ID | Activity Name | Original Duration | Schedule % Complete | Performance % Complete | BL Project Start | BL Project Finish | Start | Finish | Planned Value Cost | Earned Value Cost | Budgeted Total Cost | Variance - BL Project |
|---|---|---|---|---|---|---|---|---|---|---|---|---|
| MLTX-02-005-EM | Material Approval for Concrete Blocks | 15 | 100% | 100% | 03-May-26 | 19-May-26 | 28-Mar-26 A | 04-Apr-26 A | 0.00 | 0.00 | 0.00 | 39 |
| **FLOOR/WALL TILES** | | 30 | 0% | 0% | 15-Apr-26 | 19-May-26 | 19-Mar-26 A | 17-May-26 A | 0.00 | 0.00 | 0.00 | 2 |
| MLTX-02-005-EM | Material Submittal for Tilling Materials | 15 | 100% | 100% | 15-Apr-26 | 02-May-26 | 19-Mar-26 A | 12-May-26 A | 0.00 | 0.00 | 0.00 | -9 |
| MLTX-02-005-EM | Material Approval for Tilling Material | 15 | 100% | 100% | 03-May-26 | 19-May-26 | 26-Mar-26 A | 17-May-26 A | 0.00 | 0.00 | 0.00 | 2 |
| **SUSPENDED CEILING** | | 30 | 0% | 0% | 15-Apr-26 | 19-May-26 | 24-Mar-26 A | 04-Apr-26 A | 0.00 | 0.00 | 0.00 | 39 |
| MLTX-02-005-EM | Material Submittal for Suspend Ceiling | 15 | 100% | 100% | 15-Apr-26 | 02-May-26 | 24-Mar-26 A | 26-Mar-26 A | 0.00 | 0.00 | 0.00 | 31 |
| MLTX-02-005-EM | Material Approval for Suspend Ceiling | 15 | 100% | 100% | 03-May-26 | 19-May-26 | 28-Mar-26 A | 04-Apr-26 A | 0.00 | 0.00 | 0.00 | 39 |
| **DOORS/WINDOWS** | | 30 | 0% | 0% | 15-Apr-26 | 19-May-26 | 24-Mar-26 A | 04-Apr-26 A | 0.00 | 0.00 | 0.00 | 39 |
| MLTX-02-005-EM | Material Submittal for Doors/Windows | 15 | 100% | 100% | 15-Apr-26 | 02-May-26 | 24-Mar-26 A | 26-Mar-26 A | 0.00 | 0.00 | 0.00 | 31 |
| MLTX-02-005-EM | Material Approval for Doors/Windows | 15 | 100% | 100% | 03-May-26 | 19-May-26 | 28-Mar-26 A | 04-Apr-26 A | 0.00 | 0.00 | 0.00 | 39 |
| **FURNITURES** | | 30 | 0% | 0% | 15-Apr-26 | 19-May-26 | 19-Mar-26 A | 17-May-26 A | 0.00 | 0.00 | 0.00 | 2 |
| MLTX-02-005-EM | Material Submittal for Furnitures | 15 | 100% | 100% | 15-Apr-26 | 02-May-26 | 19-Mar-26 A | 13-May-26 A | 0.00 | 0.00 | 0.00 | -10 |
| MLTX-02-005-EM | Material Approval for Furnitures | 15 | 100% | 100% | 03-May-26 | 19-May-26 | 26-Mar-26 A | 17-May-26 A | 0.00 | 0.00 | 0.00 | 2 |
| **SANITARY FIXTURES** | | 30 | 0% | 0% | 15-Apr-26 | 19-May-26 | 19-Mar-26 A | 17-May-26 A | 0.00 | 0.00 | 0.00 | 2 |
| MLTX-02-005-EM | Material Submittal for Sanitary Fixtures | 15 | 100% | 100% | 15-Apr-26 | 02-May-26 | 19-Mar-26 A | 13-May-26 A | 0.00 | 0.00 | 0.00 | -10 |
| MLTX-02-005-EM | Material Approval for Sanitary Fixtures | 15 | 100% | 100% | 03-May-26 | 19-May-26 | 26-Mar-26 A | 17-May-26 A | 0.00 | 0.00 | 0.00 | 2 |
| **WATER SUPPLY PIPES** | | 30 | 0% | 0% | 15-Apr-26 | 19-May-26 | 24-Mar-26 A | 04-Apr-26 A | 0.00 | 0.00 | 0.00 | 39 |
| MLTX-02-005-EM | Material Submittal for Water Supply Pipes | 15 | 100% | 100% | 15-Apr-26 | 02-May-26 | 24-Mar-26 A | 26-Mar-26 A | 0.00 | 0.00 | 0.00 | 31 |
| MLTX-02-005-EM | Material Approval for Water Supply Pipes | 15 | 100% | 100% | 03-May-26 | 19-May-26 | 28-Mar-26 A | 04-Apr-26 A | 0.00 | 0.00 | 0.00 | 39 |
| **SEWAGE/DRAINAGE PIPES** | | 30 | 0% | 0% | 15-Apr-26 | 19-May-26 | 08-Jun-26 A | 15-Jun-26 A | 0.00 | 0.00 | 0.00 | -20 |
| MLTX-02-005-EM | Material Submittal for Sewage/Drainage Pipes | 15 | 100% | 100% | 15-Apr-26 | 02-May-26 | 08-Jun-26 A | 08-Jun-26 A | 0.00 | 0.00 | 0.00 | -29 |
| MLTX-02-005-EM | Material Approval for Sewage/Drainage Pipes | 15 | 100% | 100% | 03-May-26 | 19-May-26 | 15-Jun-26 A | 15-Jun-26 A | 0.00 | 0.00 | 0.00 | -20 |
| **PACKAGE AC UNITS** | | 30 | 0% | 0% | 03-May-26 | 09-Jun-26 | 07-Jul-26 A | 07-Jul-26 A | 0.00 | 0.00 | 0.00 | -24 |
| MLTX-02-005-EM | Material Submittal for Package AC Units | 15 | 100% | 100% | 03-May-26 | 19-May-26 | 07-Jul-26 A | 07-Jul-26 A | 0.00 | 0.00 | 0.00 | -39 |
| MLTX-02-005-EM | Material Approval for Package AC Units | 15 | 100% | 100% | 20-May-26 | 09-Jun-26 | 07-Jul-26 A | 07-Jul-26 A | 0.00 | 0.00 | 0.00 | -24 |
| **AIR DIFUSSERS/GRILLS** | | 30 | 0% | 0% | 03-May-26 | 09-Jun-26 | 27-Jul-26 A | 30-Jul-26 A | 0.00 | 0.00 | 0.00 | -44 |
| MLTX-02-005-EM | Material Submittal for Air Diffusers/Grills | 15 | 100% | 100% | 03-May-26 | 19-May-26 | 27-Jul-26 A | 27-Jul-26 A | 0.00 | 0.00 | 0.00 | -56 |
| MLTX-02-005-EM | Material Approval for Air Diffusers/Grills | 15 | 100% | 100% | 20-May-26 | 09-Jun-26 | 30-Jul-26 A | 30-Jul-26 A | 0.00 | 0.00 | 0.00 | -44 |
| **GALVANIZED DUCTS** | | 30 | 0% | 0% | 03-May-26 | 09-Jun-26 | 24-Mar-26 A | 30-Apr-26 A | 0.00 | 0.00 | 0.00 | 31 |
| MLTX-02-005-EM | Material Submittal for Galvanized Ducts | 15 | 100% | 100% | 03-May-26 | 19-May-26 | 24-Mar-26 A | 25-Apr-26 A | 0.00 | 0.00 | 0.00 | 21 |
| MLTX-02-005-EM | Material Approval for Galvanized Ducts | 15 | 100% | 100% | 20-May-26 | 09-Jun-26 | 28-Mar-26 A | 30-Apr-26 A | 0.00 | 0.00 | 0.00 | 31 |
| **EXHAUST FANS** | | 30 | 0% | 0% | 03-May-26 | 09-Jun-26 | 27-Jul-26 A | 30-Jul-26 A | 0.00 | 0.00 | 0.00 | -44 |
| MLTX-02-005-EM | Material Submittal for Exhaust Fans | 15 | 100% | 100% | 03-May-26 | 19-May-26 | 27-Jul-26 A | 27-Jul-26 A | 0.00 | 0.00 | 0.00 | -56 |
| MLTX-02-005-EM | Material Approval for Exhaust Fans | 15 | 100% | 100% | 20-May-26 | 09-Jun-26 | 30-Jul-26 A | 30-Jul-26 A | 0.00 | 0.00 | 0.00 | -44 |
| **LIGHTING FIXTURES** | | 30 | 0% | 0% | 03-May-26 | 09-Jun-26 | 07-Jul-26 A | 07-Jul-26 A | 0.00 | 0.00 | 0.00 | -24 |
| MLTX-02-005-EM | Material Submittal for Lighting Fixtures | 15 | 100% | 100% | 03-May-26 | 19-May-26 | 07-Jul-26 A | 07-Jul-26 A | 0.00 | 0.00 | 0.00 | -39 |
| MLTX-02-005-EM | Material Approval for Lighting Fixtures | 15 | 100% | 100% | 20-May-26 | 09-Jun-26 | 07-Jul-26 A | 07-Jul-26 A | 0.00 | 0.00 | 0.00 | -24 |
| **SWITCHES/SOCKETS** | | 30 | 0% | 0% | 03-May-26 | 09-Jun-26 | 27-Jul-26 A | 30-Jul-26 A | 0.00 | 0.00 | 0.00 | -44 |
| MLTX-02-005-EM | Material Submittal for Switches/Sockets | 15 | 100% | 100% | 03-May-26 | 19-May-26 | 27-Jul-26 A | 27-Jul-26 A | 0.00 | 0.00 | 0.00 | -56 |
| MLTX-02-005-EM | Material Approval for Switches/Sockets | 15 | 100% | 100% | 20-May-26 | 09-Jun-26 | 30-Jul-26 A | 30-Jul-26 A | 0.00 | 0.00 | 0.00 | -44 |
| **EARTHING SYSTEM** | | 30 | 0% | 0% | 03-May-26 | 09-Jun-26 | 24-Mar-26 A | 18-May-26 A | 0.00 | 0.00 | 0.00 | 16 |
| MLTX-02-005-EM | Material Submittal for Earthing System | 15 | 100% | 100% | 03-May-26 | 19-May-26 | 24-Mar-26 A | 14-May-26 A | 0.00 | 0.00 | 0.00 | 4 |
| MLTX-02-005-EM | Material Approval for Earthing System | 15 | 100% | 100% | 20-May-26 | 09-Jun-26 | 28-Mar-26 A | 18-May-26 A | 0.00 | 0.00 | 0.00 | 16 |
| **DISTRIBUTION PANNELS** | | 30 | 0% | 0% | 03-May-26 | 09-Jun-26 | 27-Jul-26 A | 30-Jul-26 A | 0.00 | 0.00 | 0.00 | -44 |
| MLTX-02-005-EM | Material Submittal for Distribution Panels | 15 | 100% | 100% | 03-May-26 | 19-May-26 | 27-Jul-26 A | 27-Jul-26 A | 0.00 | 0.00 | 0.00 | -56 |
| MLTX-02-005-EM | Material Approval for Distribution Panels | 15 | 100% | 100% | 20-May-26 | 09-Jun-26 | 30-Jul-26 A | 30-Jul-26 A | 0.00 | 0.00 | 0.00 | -44 |
| **PLAYGROUND WORKS** | | 84 | 0% | 0% | 15-Apr-26 | 13-Jun-26 | 19-Mar-26 A | 12-Sep-26 A | 0.00 | 0.00 | 0.00 | -78 |
| **PVC MEMBRANE** | | 30 | 0% | 0% | 15-Apr-26 | 19-May-26 | 24-Mar-26 A | 04-Apr-26 A | 0.00 | 0.00 | 0.00 | 39 |
| MLTX-02-005-EM | Material Submittal for PVC Membrane | 15 | 100% | 100% | 15-Apr-26 | 02-May-26 | 24-Mar-26 A | 26-Mar-26 A | 0.00 | 0.00 | 0.00 | 31 |
| MLTX-02-005-EM | Material Approval for PVC Membrane | 15 | 100% | 100% | 03-May-26 | 19-May-26 | 28-Mar-26 A | 04-Apr-26 A | 0.00 | 0.00 | 0.00 | 39 |
| **STEEL TENSION CABLES** | | 30 | 0% | 0% | 15-Apr-26 | 19-May-26 | 26-Aug-26 A | 26-Aug-26 A | 0.00 | 0.00 | 0.00 | -82 |
| MLTX-02-005-EM | Material Submittal for Steel Tension Cables | 15 | 100% | 100% | 15-Apr-26 | 02-May-26 | 26-Aug-26 A | 26-Aug-26 A | 0.00 | 0.00 | 0.00 | -97 |
| MLTX-02-005-EM | Material Approval for Steel Tension Cables | 15 | 100% | 100% | 03-May-26 | 19-May-26 | 26-Aug-26 A | 26-Aug-26 A | 0.00 | 0.00 | 0.00 | -82 |
| **EMERGENCY DOORS** | | 28 | 0% | 0% | 15-Apr-26 | 19-May-26 | 26-Aug-26 A | 12-Sep-26 A | 0.00 | 0.00 | 0.00 | -96 |
| MLTX-02-005-EM | Material Submittal for Emergency Doors | 15 | 100% | 100% | 15-Apr-26 | 02-May-26 | 26-Aug-26 A | 26-Aug-26 A | 0.00 | 0.00 | 0.00 | -97 |
| MLTX-02-005-EM | Material Approval for Emergency Doors | 15 | 100% | 100% | 03-May-26 | 19-May-26 | 12-Sep-26 A | 12-Sep-26 A | 0.00 | 0.00 | 0.00 | -96 |
| **PRESSURE UNITS** | | 30 | 0% | 0% | 15-Apr-26 | 19-May-26 | 12-Sep-26 A | 12-Sep-26 A | 0.00 | 0.00 | 0.00 | -96 |
| MLTX-02-005-EM | Material Submittal for Pressure Units | 15 | 100% | 100% | 15-Apr-26 | 02-May-26 | 12-Sep-26 A | 12-Sep-26 A | 0.00 | 0.00 | 0.00 | -111 |
| MLTX-02-005-EM | Material Approval for Pressure Units | 15 | 100% | 100% | 03-May-26 | 19-May-26 | 12-Sep-26 A | 12-Sep-26 A | 0.00 | 0.00 | 0.00 | -96 |
| **AIR LOCK DOORS** | | 28 | 0% | 0% | 15-Apr-26 | 19-May-26 | 26-Aug-26 A | 12-Sep-26 A | 0.00 | 0.00 | 0.00 | -96 |
| MLTX-02-005-EM | Material Submittal for Lock Doors | 15 | 100% | 100% | 15-Apr-26 | 02-May-26 | 26-Aug-26 A | 26-Aug-26 A | 0.00 | 0.00 | 0.00 | -97 |
| MLTX-02-005-EM | Material Approval for Lock Doors | 15 | 100% | 100% | 03-May-26 | 19-May-26 | 12-Sep-26 A | 12-Sep-26 A | 0.00 | 0.00 | 0.00 | -96 |
| **ARTIFICIAL TURF** | | 30 | 0% | 0% | 15-Apr-26 | 19-May-26 | 19-Mar-26 A | 19-May-26 A | 0.00 | 0.00 | 0.00 | 0 |
| MLTX-02-005-EM | Material Submittal for Artificial TURF | 15 | 100% | 100% | 15-Apr-26 | 02-May-26 | 19-Mar-26 A | 14-May-26 A | 0.00 | 0.00 | 0.00 | -11 |

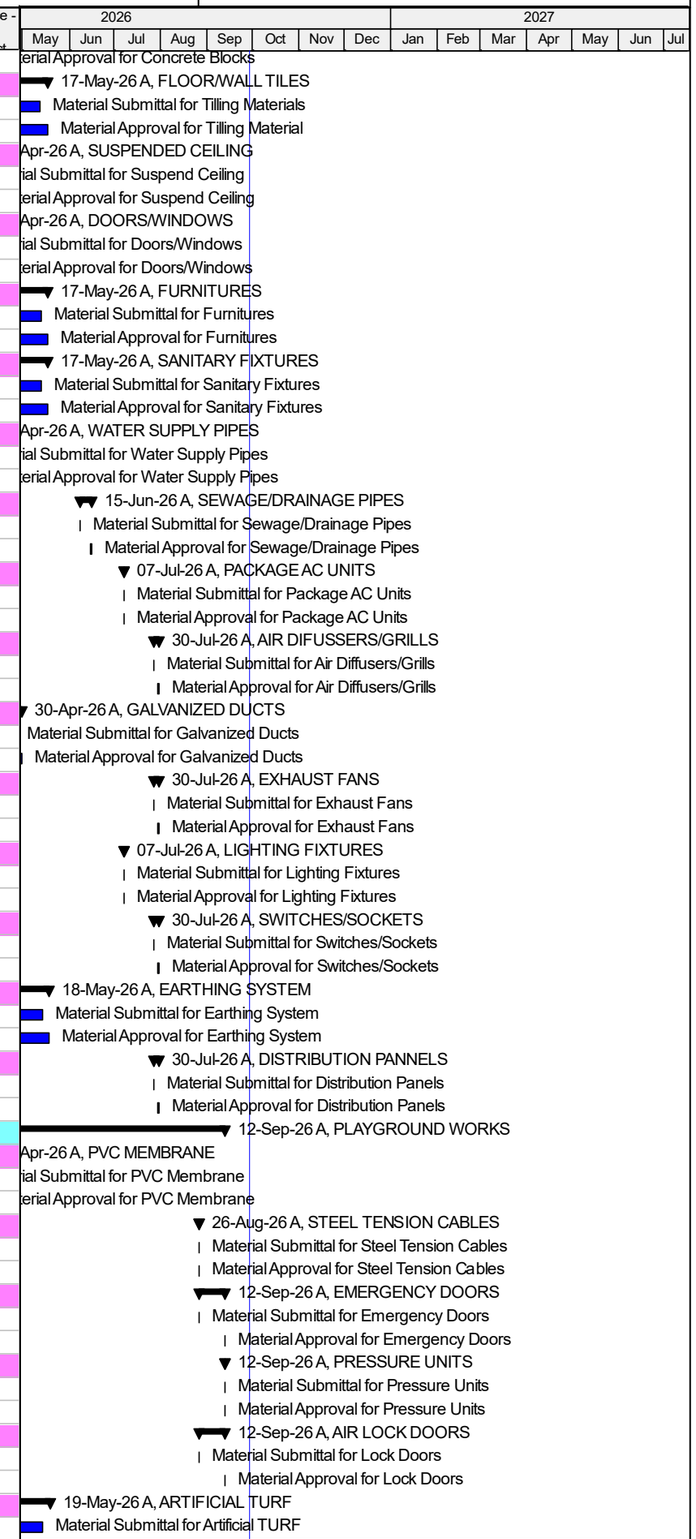


Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary




TASK filter: All Activities

© Oracle Corporation

# MLTX-02-005 - Playground Initiative for Eastern Region (Arar-Hasa osis -Dammam)

**Updateded schedule**
**D.D 28-09-2026**

| Activity ID | Activity Name | Original Duration | Schedule % Complete | Performance % Complete | BL Project Start | BL Project Finish | Start | Finish | Planned Value Cost | Earned Value Cost | Budgeted Total Cost | Variance - BL Project |
|---|---|---|---|---|---|---|---|---|---|---|---|---|
| MLTX-02-005-EM | Material Approval for Artificial TURF | 15 | 100% | 100% | 03-May-26 | 19-May-26 | 26-Mar-26 A | 19-May-26 A | 0.00 | 0.00 | 0.00 | 0 |
| **RUBBER GRANULES** | | 42 | 0% | 0% | 22-Apr-26 | 13-Jun-26 | 19-Mar-26 A | 19-May-26 A | 0.00 | 0.00 | 0.00 | 18 |
| MLTX-02-005-EM | Material Submittal for Rubber Granules | 21 | 100% | 100% | 22-Apr-26 | 16-May-26 | 19-Mar-26 A | 14-May-26 A | 0.00 | 0.00 | 0.00 | 1 |
| MLTX-02-005-EM | Material Approval for Rubber Granules | 21 | 100% | 100% | 17-May-26 | 13-Jun-26 | 26-Mar-26 A | 19-May-26 A | 0.00 | 0.00 | 0.00 | 18 |
| **PADEL GLASS** | | 30 | 0% | 0% | 15-Apr-26 | 19-May-26 | 19-Mar-26 A | 19-May-26 A | 0.00 | 0.00 | 0.00 | 0 |
| MLTX-02-005-EM | Material Submittal for Padel Glass | 15 | 100% | 100% | 15-Apr-26 | 02-May-26 | 19-Mar-26 A | 14-May-26 A | 0.00 | 0.00 | 0.00 | -11 |
| MLTX-02-005-EM | Material Approval for Padel Glass | 15 | 100% | 100% | 03-May-26 | 19-May-26 | 26-Mar-26 A | 19-May-26 A | 0.00 | 0.00 | 0.00 | 0 |
| **PADEL WIRE MESH/STEEL SETS** | | 30 | 0% | 0% | 15-Apr-26 | 19-May-26 | 19-Mar-26 A | 19-May-26 A | 0.00 | 0.00 | 0.00 | 0 |
| MLTX-02-005-EM | Material Submittal for Wire Mesh/Steel Sets | 15 | 100% | 100% | 15-Apr-26 | 02-May-26 | 19-Mar-26 A | 14-May-26 A | 0.00 | 0.00 | 0.00 | -11 |
| MLTX-02-005-EM | Material Approval for Wire Mesh/Steel Sets | 15 | 100% | 100% | 03-May-26 | 19-May-26 | 26-Mar-26 A | 19-May-26 A | 0.00 | 0.00 | 0.00 | 0 |
| **AGGREGATE BASE COURSE** | | 42 | 0% | 0% | 22-Apr-26 | 13-Jun-26 | 19-Mar-26 A | 07-May-26 A | 0.00 | 0.00 | 0.00 | 28 |
| MLTX-02-005-EM | Material Submittal for Aggregate Base Course | 21 | 100% | 100% | 22-Apr-26 | 16-May-26 | 19-Mar-26 A | 04-May-26 A | 0.00 | 0.00 | 0.00 | 10 |
| MLTX-02-005-EM | Material Approval for Aggregate Base Course | 21 | 100% | 100% | 17-May-26 | 13-Jun-26 | 26-Mar-26 A | 07-May-26 A | 0.00 | 0.00 | 0.00 | 28 |
| **BITUMINOUS BASE & WEARING COURSE** | | 30 | 0% | 0% | 03-May-26 | 09-Jun-26 | 24-Mar-26 A | 07-May-26 A | 0.00 | 0.00 | 0.00 | 25 |
| MLTX-02-005-EM | Material Submittal for Bituminous Base & Wearing Cource | 15 | 100% | 100% | 03-May-26 | 19-May-26 | 24-Mar-26 A | 04-May-26 A | 0.00 | 0.00 | 0.00 | 13 |
| MLTX-02-005-EM | Material Approval for the Site | 15 | 100% | 100% | 20-May-26 | 09-Jun-26 | 28-Mar-26 A | 07-May-26 A | 0.00 | 0.00 | 0.00 | 25 |
| **INTERLOCKING PAVING** | | 30 | 0% | 0% | 03-May-26 | 09-Jun-26 | 24-Mar-26 A | 07-May-26 A | 0.00 | 0.00 | 0.00 | 25 |
| MLTX-02-005-EM | Material Submittal for Interlocking Block Pavers | 15 | 100% | 100% | 03-May-26 | 19-May-26 | 24-Mar-26 A | 04-May-26 A | 0.00 | 0.00 | 0.00 | 13 |
| MLTX-02-005-EM | Material Approval for Interlocking Block Pavers | 15 | 100% | 100% | 20-May-26 | 09-Jun-26 | 28-Mar-26 A | 07-May-26 A | 0.00 | 0.00 | 0.00 | 25 |
| **MARKING PAINT** | | 30 | 0% | 0% | 03-May-26 | 09-Jun-26 | 24-Mar-26 A | 18-May-26 A | 0.00 | 0.00 | 0.00 | 16 |
| MLTX-02-005-EM | Material Submittal for Marking Paint | 15 | 100% | 100% | 03-May-26 | 19-May-26 | 24-Mar-26 A | 12-May-26 A | 0.00 | 0.00 | 0.00 | 6 |
| MLTX-02-005-EM | Material Approval for Marking Paint | 15 | 100% | 100% | 20-May-26 | 09-Jun-26 | 28-Mar-26 A | 18-May-26 A | 0.00 | 0.00 | 0.00 | 16 |
| **PACKAGE AC UNITS** | | 30 | 0% | 0% | 03-May-26 | 09-Jun-26 | 07-Jul-26 A | 07-Jul-26 A | 0.00 | 0.00 | 0.00 | -24 |
| MLTX-02-005-EM | Material Submittal for Package AC Units | 15 | 100% | 100% | 03-May-26 | 19-May-26 | 07-Jul-26 A | 07-Jul-26 A | 0.00 | 0.00 | 0.00 | -39 |
| MLTX-02-005-EM | Material Approval for Package AC Units | 15 | 100% | 100% | 20-May-26 | 09-Jun-26 | 07-Jul-26 A | 07-Jul-26 A | 0.00 | 0.00 | 0.00 | -24 |
| **AIR DIFUSSERS/GRILLS** | | 30 | 0% | 0% | 03-May-26 | 09-Jun-26 | 12-Sep-26 A | 12-Sep-26 A | 0.00 | 0.00 | 0.00 | -81 |
| MLTX-02-005-EM | Material Submittal for Air Difussers/Grills | 15 | 100% | 100% | 03-May-26 | 19-May-26 | 12-Sep-26 A | 12-Sep-26 A | 0.00 | 0.00 | 0.00 | -96 |
| MLTX-02-005-EM | Material Approval for Air Difussers/Grills | 15 | 100% | 100% | 20-May-26 | 09-Jun-26 | 12-Sep-26 A | 12-Sep-26 A | 0.00 | 0.00 | 0.00 | -81 |
| **GALVANIZED DUCTS** | | 30 | 0% | 0% | 03-May-26 | 09-Jun-26 | 24-Mar-26 A | 10-May-26 A | 0.00 | 0.00 | 0.00 | 23 |
| MLTX-02-005-EM | Material Submittal for Galvanized Duct | 15 | 100% | 100% | 03-May-26 | 19-May-26 | 24-Mar-26 A | 05-May-26 A | 0.00 | 0.00 | 0.00 | 12 |
| MLTX-02-005-EM | Material Approval for Galvanized Duct | 15 | 100% | 100% | 20-May-26 | 09-Jun-26 | 28-Mar-26 A | 10-May-26 A | 0.00 | 0.00 | 0.00 | 23 |
| **EXHAUST FANS** | | 30 | 0% | 0% | 03-May-26 | 09-Jun-26 | 12-Sep-26 A | 12-Sep-26 A | 0.00 | 0.00 | 0.00 | -81 |
| MLTX-02-005-EM | Material Submittal for Exhaust Fans | 15 | 100% | 100% | 03-May-26 | 19-May-26 | 12-Sep-26 A | 12-Sep-26 A | 0.00 | 0.00 | 0.00 | -96 |
| MLTX-02-005-EM | Material Approval for Exhaust Fans | 15 | 100% | 100% | 20-May-26 | 09-Jun-26 | 12-Sep-26 A | 12-Sep-26 A | 0.00 | 0.00 | 0.00 | -81 |
| **DISTRIBUTION BOARDS** | | 30 | 0% | 0% | 03-May-26 | 09-Jun-26 | 26-Aug-26 A | 26-Aug-26 A | 0.00 | 0.00 | 0.00 | -67 |
| MLTX-02-005-EM | Material Submittal for Distribution Boards | 15 | 100% | 100% | 03-May-26 | 19-May-26 | 26-Aug-26 A | 26-Aug-26 A | 0.00 | 0.00 | 0.00 | -82 |
| MLTX-02-005-EM | Material Approval for Distribution Boards | 15 | 100% | 100% | 20-May-26 | 09-Jun-26 | 26-Aug-26 A | 26-Aug-26 A | 0.00 | 0.00 | 0.00 | -67 |
| **POWER CABLES** | | 30 | 0% | 0% | 03-May-26 | 09-Jun-26 | 24-Mar-26 A | 19-May-26 A | 0.00 | 0.00 | 0.00 | 15 |
| MLTX-02-005-EM | Material Submittal for Power Cables | 15 | 100% | 100% | 03-May-26 | 19-May-26 | 24-Mar-26 A | 14-May-26 A | 0.00 | 0.00 | 0.00 | 4 |
| MLTX-02-005-EM | Material Approval for Power Cables | 15 | 100% | 100% | 20-May-26 | 09-Jun-26 | 28-Mar-26 A | 19-May-26 A | 0.00 | 0.00 | 0.00 | 15 |
| **LIGHT FIXTURES** | | 30 | 0% | 0% | 03-May-26 | 09-Jun-26 | 07-Jul-26 A | 07-Jul-26 A | 0.00 | 0.00 | 0.00 | -24 |
| MLTX-02-005-EM | Material Submittal for Light Fixtures | 15 | 100% | 100% | 03-May-26 | 19-May-26 | 07-Jul-26 A | 07-Jul-26 A | 0.00 | 0.00 | 0.00 | -39 |
| MLTX-02-005-EM | Material Approval for Light Fixtures | 15 | 100% | 100% | 20-May-26 | 09-Jun-26 | 07-Jul-26 A | 07-Jul-26 A | 0.00 | 0.00 | 0.00 | -24 |
| **CCTV MATERIALS** | | 28 | 0% | 0% | 03-May-26 | 09-Jun-26 | 26-Aug-26 A | 12-Sep-26 A | 0.00 | 0.00 | 0.00 | -81 |
| MLTX-02-005-EM | Material Submittal for CCTV | 15 | 100% | 100% | 03-May-26 | 19-May-26 | 26-Aug-26 A | 26-Aug-26 A | 0.00 | 0.00 | 0.00 | -82 |
| MLTX-02-005-EM | Material Approval for CCTV | 15 | 100% | 100% | 20-May-26 | 09-Jun-26 | 12-Sep-26 A | 12-Sep-26 A | 0.00 | 0.00 | 0.00 | -81 |
| **POWER OUTLETS/SWITCHES** | | 30 | 0% | 0% | 03-May-26 | 09-Jun-26 | 26-Aug-26 A | 26-Aug-26 A | 0.00 | 0.00 | 0.00 | -67 |
| MLTX-02-005-EM | Material Submittal for Power Outlets/Switches | 15 | 100% | 100% | 03-May-26 | 19-May-26 | 26-Aug-26 A | 26-Aug-26 A | 0.00 | 0.00 | 0.00 | -82 |
| MLTX-02-005-EM | Material Approval for Power Outlets/Switches | 15 | 100% | 100% | 20-May-26 | 09-Jun-26 | 26-Aug-26 A | 26-Aug-26 A | 0.00 | 0.00 | 0.00 | -67 |
| **LANDSCAPE WORKS** | | 84 | 0% | 0% | 03-May-26 | 09-Jun-26 | 24-Mar-26 A | 12-Sep-26 A | 0.00 | 0.00 | 0.00 | -81 |
| **INTERLOCKING PAVING** | | 30 | 0% | 0% | 03-May-26 | 09-Jun-26 | 25-Mar-26 A | 04-Apr-26 A | 0.00 | 0.00 | 0.00 | 54 |
| MLTX-02-005-EM | Material Submittal for Interlocking Block Pavers | 15 | 100% | 100% | 03-May-26 | 19-May-26 | 25-Mar-26 A | 28-Mar-26 A | 0.00 | 0.00 | 0.00 | 45 |
| MLTX-02-005-EM | Material Approval for Interlocking Block Pavers | 15 | 100% | 100% | 20-May-26 | 09-Jun-26 | 29-Mar-26 A | 04-Apr-26 A | 0.00 | 0.00 | 0.00 | 54 |
| **CURBSTONE** | | 30 | 0% | 0% | 03-May-26 | 09-Jun-26 | 25-Mar-26 A | 04-Apr-26 A | 0.00 | 0.00 | 0.00 | 54 |
| MLTX-02-005-EM | Material Submittal for Curbstone | 15 | 100% | 100% | 03-May-26 | 19-May-26 | 25-Mar-26 A | 28-Mar-26 A | 0.00 | 0.00 | 0.00 | 45 |
| MLTX-02-005-EM | Material Approval for Curbstone | 15 | 100% | 100% | 20-May-26 | 09-Jun-26 | 29-Mar-26 A | 04-Apr-26 A | 0.00 | 0.00 | 0.00 | 54 |
| **PAVEMENT MARKING** | | 30 | 0% | 0% | 03-May-26 | 09-Jun-26 | 24-Mar-26 A | 18-May-26 A | 0.00 | 0.00 | 0.00 | 16 |
| MLTX-02-005-EM | Material Submittal for Pavement Markings | 15 | 100% | 100% | 03-May-26 | 19-May-26 | 24-Mar-26 A | 12-May-26 A | 0.00 | 0.00 | 0.00 | 6 |
| MLTX-02-005-EM | Material Approval for Pavement Markings | 15 | 100% | 100% | 20-May-26 | 09-Jun-26 | 28-Mar-26 A | 18-May-26 A | 0.00 | 0.00 | 0.00 | 16 |
| **TRAFFIC SIGNS** | | 30 | 0% | 0% | 03-May-26 | 09-Jun-26 | 24-Mar-26 A | 18-May-26 A | 0.00 | 0.00 | 0.00 | 16 |
| MLTX-02-005-EM | Material Submittal for Traffic Signs | 15 | 100% | 100% | 03-May-26 | 19-May-26 | 24-Mar-26 A | 12-May-26 A | 0.00 | 0.00 | 0.00 | 6 |
| MLTX-02-005-EM | Material Approval for Traffic Signs | 15 | 100% | 100% | 20-May-26 | 09-Jun-26 | 28-Mar-26 A | 18-May-26 A | 0.00 | 0.00 | 0.00 | 16 |
| **IRRIGATION PIPES/SPRINKLERS** | | 30 | 0% | 0% | 03-May-26 | 09-Jun-26 | 12-Sep-26 A | 12-Sep-26 A | 0.00 | 0.00 | 0.00 | -81 |
| MLTX-02-005-EM | Material Submittal for Irrigation Pipes/Sprinkles | 15 | 100% | 100% | 03-May-26 | 19-May-26 | 12-Sep-26 A | 12-Sep-26 A | 0.00 | 0.00 | 0.00 | -96 |

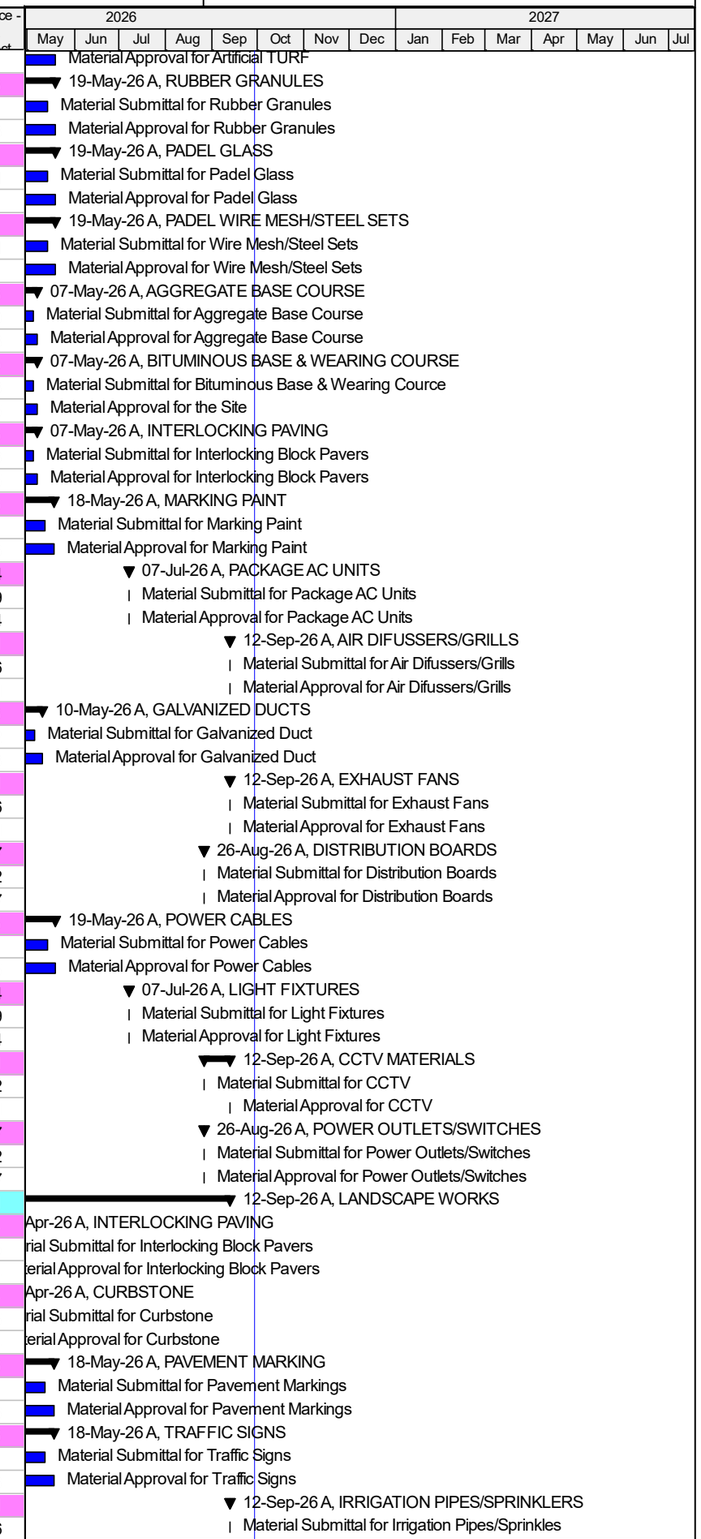




© Oracle Corporation

# MLTX-02-005 - Playground Initiative for Eastern Region (Arar-Hasa osis -Dammam)

**Updateded schedule**
**D.D 28-09-2026**

| Activity ID | Activity Name | Original Duration | Schedule % Complete | Performance % Complete | BL Project Start | BL Project Finish | Start | Finish | Planned Value Cost | Earned Value Cost | Budgeted Total Cost | Variance - BL Project |
|---|---|---|---|---|---|---|---|---|---|---|---|---|
| MLTX-02-005-EN | Material Approval for Irrigation Pipes/Sprinkles | 15 | 100% | 100% | 20-May-26 | 09-Jun-26 | 12-Sep-26 A | 12-Sep-26 A | 0.00 | 0.00 | 0.00 | -81 |
| **AGRICULTURE SOIL** | | 30 | 0% | 0% | 03-May-26 | 09-Jun-26 | 24-Mar-26 A | 21-May-26 A | 0.00 | 0.00 | 0.00 | 13 |
| MLTX-02-005-EN | Material Submittal for Agriculture Soil | 15 | 100% | 100% | 03-May-26 | 19-May-26 | 24-Mar-26 A | 16-May-26 A | 0.00 | 0.00 | 0.00 | 3 |
| MLTX-02-005-EN | Material Approval for Agriculture Soil | 15 | 100% | 100% | 20-May-26 | 09-Jun-26 | 28-Mar-26 A | 21-May-26 A | 0.00 | 0.00 | 0.00 | 13 |
| **TRACK SURFACE** | | 30 | 0% | 0% | 03-May-26 | 09-Jun-26 | 12-Sep-26 A | 12-Sep-26 A | 0.00 | 0.00 | 0.00 | -81 |
| MLTX-02-005-EN | Material Submittal for Track Surface | 15 | 100% | 100% | 03-May-26 | 19-May-26 | 12-Sep-26 A | 12-Sep-26 A | 0.00 | 0.00 | 0.00 | -96 |
| MLTX-02-005-EN | Material Approval for Track Surface | 15 | 100% | 100% | 20-May-26 | 09-Jun-26 | 12-Sep-26 A | 12-Sep-26 A | 0.00 | 0.00 | 0.00 | -81 |
| **GRASS/TREES** | | 30 | 0% | 0% | 03-May-26 | 09-Jun-26 | 24-Mar-26 A | 21-May-26 A | 0.00 | 0.00 | 0.00 | 13 |
| MLTX-02-005-EN | Material Submittal for Grass/Trees | 15 | 100% | 100% | 03-May-26 | 19-May-26 | 24-Mar-26 A | 16-May-26 A | 0.00 | 0.00 | 0.00 | 3 |
| MLTX-02-005-EN | Material Approval for Grass/Trees | 15 | 100% | 100% | 20-May-26 | 09-Jun-26 | 28-Mar-26 A | 21-May-26 A | 0.00 | 0.00 | 0.00 | 13 |
| **CABLES** | | 30 | 0% | 0% | 03-May-26 | 09-Jun-26 | 24-Mar-26 A | 19-May-26 A | 0.00 | 0.00 | 0.00 | 15 |
| MLTX-02-005-EN | Material Submittal for Cables | 15 | 100% | 100% | 03-May-26 | 19-May-26 | 24-Mar-26 A | 14-May-26 A | 0.00 | 0.00 | 0.00 | 4 |
| MLTX-02-005-EN | Material Approval for Cables | 15 | 100% | 100% | 20-May-26 | 09-Jun-26 | 28-Mar-26 A | 19-May-26 A | 0.00 | 0.00 | 0.00 | 15 |
| **LIGHT POLES** | | 30 | 0% | 0% | 03-May-26 | 09-Jun-26 | 11-Jul-26 A | 11-Jul-26 A | 0.00 | 0.00 | 0.00 | -27 |
| MLTX-02-005-EN | Material Submittal for Lighting poles | 15 | 100% | 100% | 03-May-26 | 19-May-26 | 11-Jul-26 A | 11-Jul-26 A | 0.00 | 0.00 | 0.00 | -42 |
| MLTX-02-005-EN | Material Approval for Lighting poles | 15 | 100% | 100% | 20-May-26 | 09-Jun-26 | 11-Jul-26 A | 11-Jul-26 A | 0.00 | 0.00 | 0.00 | -27 |
| **PROCUREMENT** | | 183 | 0% | 0% | 20-May-26 | 04-Nov-26 | 04-Apr-26 A | 13-Feb-27 | 0.00 | 0.00 | 0.00 | -86 |
| **SHORT LEAD ITEM** | | 183 | 0% | 0% | 20-May-26 | 20-Oct-26 | 04-Apr-26 A | 13-Feb-27 | 0.00 | 0.00 | 0.00 | -99 |
| **TOILET/SERVICE WORKS** | | 94 | 0% | 0% | 20-May-26 | 10-Aug-26 | 04-Apr-26 A | 01-Nov-26 | 0.00 | 0.00 | 0.00 | -70 |
| **STEEL REINFORCEMENT** | | 55 | 0% | 0% | 20-May-26 | 03-Jun-26 | 04-Apr-26 A | 07-Jul-26 A | 0.00 | 0.00 | 0.00 | -29 |
| MLTX-02-005-PR-1 | Material Delivery of Steel Reinforcement | 5 | 100% | 100% | 30-May-26 | 03-Jun-26 | 07-Jul-26 A | 07-Jul-26 A | 0.00 | 0.00 | 0.00 | -29 |
| MLTX-02-005-PR-9 | PO for Steel Reinforcement | 5 | 100% | 100% | 20-May-26 | 25-May-26 | 04-Apr-26 A | 18-May-26 A | 0.00 | 0.00 | 0.00 | 6 |
| **CONCRETE BLOCKS** | | 60 | 0% | 0% | 30-May-26 | 13-Jun-26 | 09-Apr-26 A | 07-Jul-26 A | 0.00 | 0.00 | 0.00 | -21 |
| MLTX-02-005-PR-1 | PO for Concrete Blocks | 5 | 100% | 100% | 30-May-26 | 03-Jun-26 | 09-Apr-26 A | 18-May-26 A | 0.00 | 0.00 | 0.00 | 11 |
| MLTX-02-005-PR-1 | Material Delivery of Concrete Blocks | 8 | 100% | 100% | 04-Jun-26 | 13-Jun-26 | 07-Jul-26 A | 07-Jul-26 A | 0.00 | 0.00 | 0.00 | -21 |
| **FLOOR/WALL TILES** | | 18 | 0% | 0% | 04-Jun-26 | 24-Jun-26 | 18-Aug-26 A | 20-Aug-26 A | 0.00 | 0.00 | 0.00 | -49 |
| MLTX-02-005-PR-1 | PO for Tilling Materials | 5 | 100% | 100% | 04-Jun-26 | 09-Jun-26 | 18-Aug-26 A | 18-Aug-26 A | 0.00 | 0.00 | 0.00 | -60 |
| MLTX-02-005-PR-1 | Material Delivery of Tailling Material | 13 | 100% | 100% | 10-Jun-26 | 24-Jun-26 | 20-Aug-26 A | 20-Aug-26 A | 0.00 | 0.00 | 0.00 | -49 |
| **SUSPENDED CEILING** | | 27 | 0% | 0% | 21-Jul-26 | 10-Aug-26 | 28-Jul-26 A | 18-Aug-26 A | 0.00 | 0.00 | 0.00 | -7 |
| MLTX-02-005-PR-1 | PO for Suspend Ceiling | 5 | 100% | 100% | 21-Jul-26 | 26-Jul-26 | 28-Jul-26 A | 28-Jul-26 A | 0.00 | 0.00 | 0.00 | -2 |
| MLTX-02-005-PR-1 | Material Delivery of Suspend Ceiling | 13 | 100% | 100% | 27-Jul-26 | 10-Aug-26 | 18-Aug-26 A | 18-Aug-26 A | 0.00 | 0.00 | 0.00 | -7 |
| **DOORS/WINDOWS** | | 20 | 0% | 0% | 10-Jun-26 | 02-Jul-26 | 15-Sep-26 A | 20-Sep-26 A | 0.00 | 0.00 | 0.00 | -68 |
| MLTX-02-005-PR-1 | PO for Doors/Windows | 5 | 100% | 100% | 10-Jun-26 | 15-Jun-26 | 15-Sep-26 A | 15-Sep-26 A | 0.00 | 0.00 | 0.00 | -79 |
| MLTX-02-005-PR-1 | Material Delivery for Doors/Windows | 15 | 100% | 100% | 16-Jun-26 | 02-Jul-26 | 20-Sep-26 A | 20-Sep-26 A | 0.00 | 0.00 | 0.00 | -68 |
| **WATER SUPPLY PIPES** | | 19 | 0% | 0% | 16-Jun-26 | 29-Jun-26 | 07-Jul-26 A | 08-Jul-26 A | 0.00 | 0.00 | 0.00 | -8 |
| MLTX-02-005-PR-1 | PO for Water Supply Pipes | 5 | 100% | 100% | 16-Jun-26 | 21-Jun-26 | 07-Jul-26 A | 07-Jul-26 A | 0.00 | 0.00 | 0.00 | -14 |
| MLTX-02-005-PR-1 | Material Delivery for Water Supply Pipes | 7 | 100% | 100% | 22-Jun-26 | 29-Jun-26 | 08-Jul-26 A | 08-Jul-26 A | 0.00 | 0.00 | 0.00 | -8 |
| **SEWAGE/DRAINAGE PIPES** | | 12 | 0% | 0% | 16-Jun-26 | 29-Jun-26 | 13-Jun-26 A | 20-Jun-26 A | 0.00 | 0.00 | 0.00 | 8 |
| MLTX-02-005-PR-1 | PO for Sewage/Drainage Pipes | 5 | 100% | 100% | 16-Jun-26 | 21-Jun-26 | 20-Jun-26 A | 20-Jun-26 A | 0.00 | 0.00 | 0.00 | 1 |
| MLTX-02-005-PR-1 | Material Delivery for Sewage/Drainage Pipes | 7 | 100% | 100% | 22-Jun-26 | 29-Jun-26 | 13-Jun-26 A | 13-Jun-26 A | 0.00 | 0.00 | 0.00 | 14 |
| **SANITARY FIXTURES** | | 18 | 0% | 0% | 22-Jun-26 | 12-Jul-26 | 28-Jul-26 A | 28-Jul-26 A | 0.00 | 0.00 | 0.00 | -14 |
| MLTX-02-005-PR-1 | PO for Sanitary Fixtures | 5 | 100% | 100% | 22-Jun-26 | 27-Jun-26 | 28-Jul-26 A | 28-Jul-26 A | 0.00 | 0.00 | 0.00 | -27 |
| MLTX-02-005-PR-1 | Material Delivery for Sanitary Fixtures | 13 | 100% | 100% | 28-Jun-26 | 12-Jul-26 | 28-Jul-26 A | 28-Jul-26 A | 0.00 | 0.00 | 0.00 | -14 |
| **PACKAGE AC UNITS** | | 20 | 0% | 0% | 28-Jun-26 | 20-Jul-26 | 07-Jul-26 A | 07-Jul-26 A | 0.00 | 0.00 | 0.00 | 11 |
| MLTX-02-005-PR-1 | PO for Package AC Units | 5 | 100% | 100% | 28-Jun-26 | 02-Jul-26 | 07-Jul-26 A | 07-Jul-26 A | 0.00 | 0.00 | 0.00 | -4 |
| MLTX-02-005-PR-1 | Material Delivery for Package AC Units | 15 | 100% | 100% | 04-Jul-26 | 20-Jul-26 | 07-Jul-26 A | 07-Jul-26 A | 0.00 | 0.00 | 0.00 | 11 |
| **AIR DIFUSSERS/GRILLS** | | 20 | 0% | 0% | 28-Jun-26 | 20-Jul-26 | 18-Aug-26 A | 20-Aug-26 A | 0.00 | 0.00 | 0.00 | -27 |
| MLTX-02-005-PR-1 | PO for Air Diffusers/Grills | 5 | 100% | 100% | 28-Jun-26 | 02-Jul-26 | 18-Aug-26 A | 18-Aug-26 A | 0.00 | 0.00 | 0.00 | -40 |
| MLTX-02-005-PR-1 | Material Delivery for Air Diffusers/Grills | 15 | 100% | 100% | 04-Jul-26 | 20-Jul-26 | 20-Aug-26 A | 20-Aug-26 A | 0.00 | 0.00 | 0.00 | -27 |
| **GALVANIZED DUCTS** | | 20 | 0% | 0% | 28-Jun-26 | 20-Jul-26 | 20-Aug-26 A | 20-Aug-26 A | 0.00 | 0.00 | 0.00 | -27 |
| MLTX-02-005-PR-1 | PO for Galvanized Ducts | 5 | 100% | 100% | 28-Jun-26 | 02-Jul-26 | 20-Aug-26 A | 20-Aug-26 A | 0.00 | 0.00 | 0.00 | -42 |
| MLTX-02-005-PR-1 | Material Delivery for Galvanized Ducts | 15 | 100% | 100% | 04-Jul-26 | 20-Jul-26 | 20-Aug-26 A | 20-Aug-26 A | 0.00 | 0.00 | 0.00 | -27 |
| **EXHAUST FANS** | | 15 | 0% | 0% | 28-Jun-26 | 14-Jul-26 | 18-Aug-26 A | 18-Aug-26 A | 0.00 | 0.00 | 0.00 | -30 |
| MLTX-02-005-PR-1 | PO for Exhaust Fans | 5 | 100% | 100% | 28-Jun-26 | 02-Jul-26 | 18-Aug-26 A | 18-Aug-26 A | 0.00 | 0.00 | 0.00 | -40 |
| MLTX-02-005-PR-1 | Material Delivery for Exhaust Fans | 10 | 100% | 100% | 04-Jul-26 | 14-Jul-26 | 18-Aug-26 A | 18-Aug-26 A | 0.00 | 0.00 | 0.00 | -30 |
| **LIGHTING FIXTURES** | | 25 | 0% | 0% | 04-Jul-26 | 20-Jul-26 | 07-Jul-26 A | 10-Oct-26 | 0.00 | 0.00 | 0.00 | -69 |
| MLTX-02-005-PR-1 | PO for Lighting Fixtures | 5 | 100% | 100% | 04-Jul-26 | 08-Jul-26 | 07-Jul-26 A | 07-Jul-26 A | 0.00 | 0.00 | 0.00 | 1 |
| MLTX-02-005-PR-1 | Material Delivery for Lighting Fixtures | 10 | 100% | 0% | 09-Jul-26 | 20-Jul-26 | 29-Sep-26 | 10-Oct-26 | 0.00 | 0.00 | 0.00 | -69 |
| **SWITCHES/SOCKETS** | | 12 | 0% | 0% | 09-Jul-26 | 22-Jul-26 | 29-Sep-26 | 12-Oct-26 | 0.00 | 0.00 | 0.00 | -69 |
| MLTX-02-005-PR-1 | PO for Switches/Sockets | 5 | 100% | 0% | 09-Jul-26 | 14-Jul-26 | 29-Sep-26 | 04-Oct-26 | 0.00 | 0.00 | 0.00 | -69 |
| MLTX-02-005-PR-1 | Material Delivery for Switches/Sockets | 7 | 100% | 0% | 15-Jul-26 | 22-Jul-26 | 05-Oct-26 | 12-Oct-26 | 0.00 | 0.00 | 0.00 | -69 |
| **EARTHING SYSTEM** | | 27 | 0% | 0% | 10-Jun-26 | 11-Jul-26 | 10-Aug-26 A | 10-Aug-26 A | 0.00 | 0.00 | 0.00 | -26 |
| MLTX-02-005-PR-1 | PO for Earthing System | 5 | 100% | 100% | 10-Jun-26 | 15-Jun-26 | 10-Aug-26 A | 10-Aug-26 A | 0.00 | 0.00 | 0.00 | -48 |
| MLTX-02-005-PR-1 | Material Delivery for Earthing System | 15 | 100% | 100% | 24-Jun-26 | 11-Jul-26 | 10-Aug-26 A | 10-Aug-26 A | 0.00 | 0.00 | 0.00 | -26 |

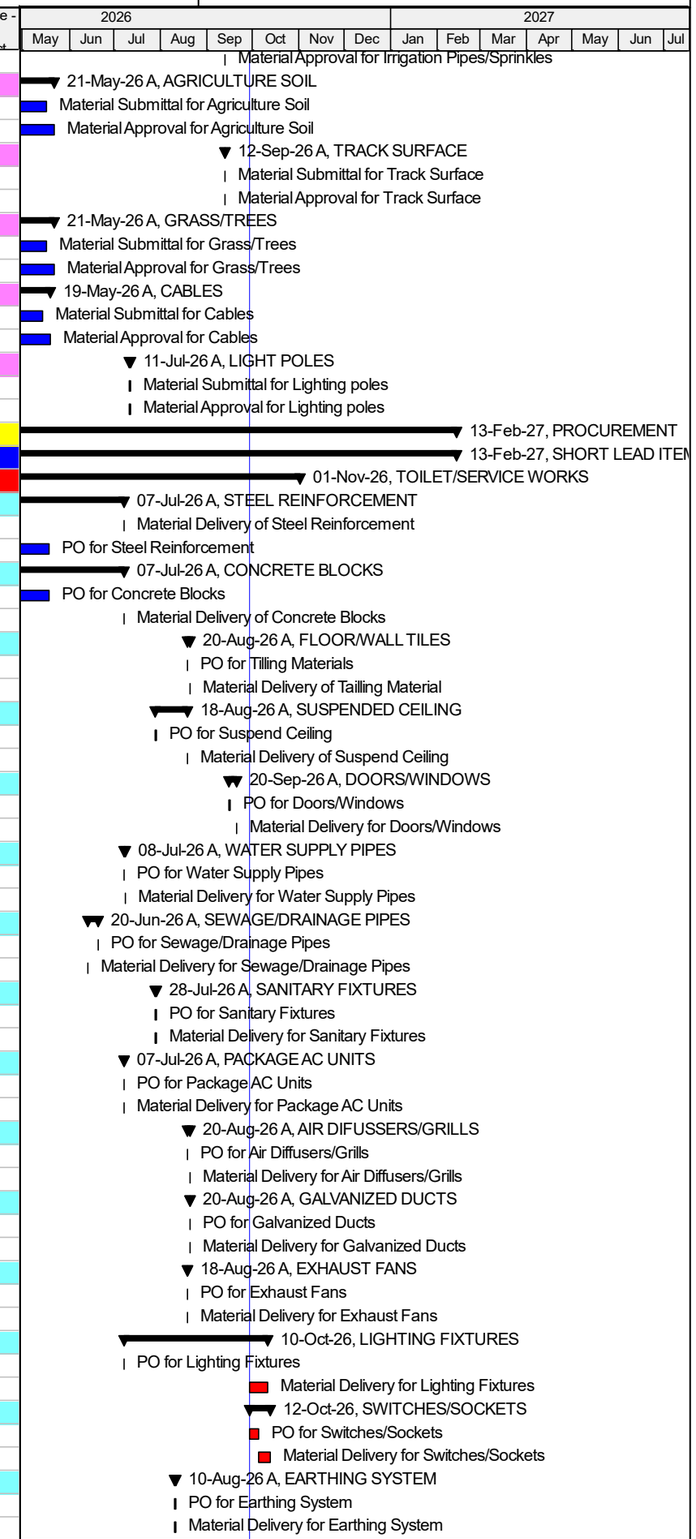


Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary




TASK filter: All Activities

© Oracle Corporation

# MLTX-02-005 - Playground Initiative for Eastern Region (Arar-Hasa osis -Dammam)

**Updateded schedule**
**D.D 28-09-2026**

| Activity ID | Activity Name | Original Duration | Schedule % Complete | Performance % Complete | BL Project Start | BL Project Finish | Start | Finish | Planned Value Cost | Earned Value Cost | Budgeted Total Cost | Variance - BL Project |
|---|---|---|---|---|---|---|---|---|---|---|---|---|
| **DISTRIBUTION PANNELS** | | 20 | 0% | 0% | 10-Jun-26 | 02-Jul-26 | 29-Sep-26 | 21-Oct-26 | 0.00 | 0.00 | 0.00 | -94 |
| MLTX-02-005-PR-1 | PO for Distribution Panels | 5 | 100% | 0% | 10-Jun-26 | 15-Jun-26 | 29-Sep-26 | 04-Oct-26 | 0.00 | 0.00 | 0.00 | -94 |
| MLTX-02-005-PR-1 | Material Delivery for Distribution Panels | 15 | 100% | 0% | 16-Jun-26 | 02-Jul-26 | 05-Oct-26 | 21-Oct-26 | 0.00 | 0.00 | 0.00 | -94 |
| **FURNITURES** | | 29 | 0% | 0% | 04-Jul-26 | 05-Aug-26 | 29-Sep-26 | 01-Nov-26 | 0.00 | 0.00 | 0.00 | -74 |
| MLTX-02-005-PR-1 | PO for Furnitures | 9 | 100% | 0% | 04-Jul-26 | 13-Jul-26 | 29-Sep-26 | 08-Oct-26 | 0.00 | 0.00 | 0.00 | -74 |
| MLTX-02-005-PR-1 | Material Delivery for Furnitures | 20 | 100% | 0% | 14-Jul-26 | 05-Aug-26 | 10-Oct-26 | 01-Nov-26 | 0.00 | 0.00 | 0.00 | -74 |
| **PLAYGROUND WORKS** | | 115 | 0% | 0% | 20-May-26 | 19-Aug-26 | 04-Apr-26 A | 25-Nov-26 | 0.00 | 0.00 | 0.00 | -83 |
| **PVC MEMBRANE** | | 19 | 0% | 0% | 20-May-26 | 01-Jun-26 | 04-Apr-26 A | 03-Oct-26 | 0.00 | 0.00 | 0.00 | -105 |
| MLTX-02-005-PR-1 | PO for PVC Membrane | 4 | 100% | 100% | 20-May-26 | 24-May-26 | 04-Apr-26 A | 19-May-26 A | 0.00 | 0.00 | 0.00 | 4 |
| MLTX-02-005-PR-1 | Material Delivery for PVC Membrane | 4 | 100% | 0% | 25-May-26 | 01-Jun-26 | 29-Sep-26 | 03-Oct-26 | 0.00 | 0.00 | 0.00 | -105 |
| **ARTIFICIAL TURF** | | 27 | 0% | 0% | 20-May-26 | 11-Jun-26 | 04-Apr-26 A | 12-Oct-26 | 0.00 | 0.00 | 0.00 | -104 |
| MLTX-02-005-PR-1 | PO for Artificial TURF | 5 | 100% | 100% | 20-May-26 | 25-May-26 | 04-Apr-26 A | 19-May-26 A | 0.00 | 0.00 | 0.00 | 5 |
| MLTX-02-005-PR-1 | Material Delivery for Artificial TURF | 12 | 100% | 0% | 30-May-26 | 11-Jun-26 | 29-Sep-26 | 12-Oct-26 | 0.00 | 0.00 | 0.00 | -104 |
| **RUBBER GRANULES** | | 12 | 0% | 0% | 14-Jun-26 | 02-Jul-26 | 04-Apr-26 A | 12-Oct-26 | 0.00 | 0.00 | 0.00 | -86 |
| MLTX-02-005-PR-1 | PO for Rubber Granules | 5 | 100% | 100% | 14-Jun-26 | 18-Jun-26 | 04-Apr-26 A | 19-May-26 A | 0.00 | 0.00 | 0.00 | 23 |
| MLTX-02-005-PR-1 | Material Delivery for Rubber Granules | 12 | 100% | 0% | 20-Jun-26 | 02-Jul-26 | 29-Sep-26 | 12-Oct-26 | 0.00 | 0.00 | 0.00 | -86 |
| **PADEL GLASS** | | 33 | 0% | 0% | 20-May-26 | 18-Jun-26 | 04-Apr-26 A | 19-Oct-26 | 0.00 | 0.00 | 0.00 | -104 |
| MLTX-02-005-PR-1 | PO for Padel Glass | 5 | 100% | 100% | 20-May-26 | 25-May-26 | 04-Apr-26 A | 19-May-26 A | 0.00 | 0.00 | 0.00 | 5 |
| MLTX-02-005-PR-1 | Material Delivery for Padel Glass | 18 | 100% | 0% | 30-May-26 | 18-Jun-26 | 29-Sep-26 | 19-Oct-26 | 0.00 | 0.00 | 0.00 | -104 |
| **PADEL WIRE MESH/STEEL SETS** | | 25 | 0% | 0% | 30-May-26 | 21-Jun-26 | 09-Apr-26 A | 15-Oct-26 | 0.00 | 0.00 | 0.00 | -99 |
| MLTX-02-005-PR-1 | PO for Wire Mesh/Steel Sets | 5 | 100% | 100% | 30-May-26 | 03-Jun-26 | 09-Apr-26 A | 19-May-26 A | 0.00 | 0.00 | 0.00 | 10 |
| MLTX-02-005-PR-1 | Material Delivery for Wire Mesh/Steel Sets | 15 | 100% | 0% | 04-Jun-26 | 21-Jun-26 | 29-Sep-26 | 15-Oct-26 | 0.00 | 0.00 | 0.00 | -99 |
| **AGGREGATE BASE COURSE** | | 73 | 0% | 0% | 14-Jun-26 | 27-Jun-26 | 04-Apr-26 A | 07-Jul-26 A | 0.00 | 0.00 | 0.00 | -9 |
| MLTX-02-005-PR-9 | PO for Aggregate Base Course | 5 | 100% | 100% | 14-Jun-26 | 18-Jun-26 | 04-Apr-26 A | 14-May-26 A | 0.00 | 0.00 | 0.00 | 27 |
| MLTX-02-005-PR-9 | Material Delivery for Aggregate Base Course | 7 | 100% | 100% | 20-Jun-26 | 27-Jun-26 | 07-Jul-26 A | 07-Jul-26 A | 0.00 | 0.00 | 0.00 | -9 |
| **BITUMINOUS BASE & WEARING COURSE** | | 12 | 0% | 0% | 10-Jun-26 | 23-Jun-26 | 15-Sep-26 A | 21-Sep-26 A | 0.00 | 0.00 | 0.00 | -77 |
| MLTX-02-005-PR-1 | PO for Bituminous Base & Wearing Course | 5 | 100% | 100% | 10-Jun-26 | 15-Jun-26 | 15-Sep-26 A | 15-Sep-26 A | 0.00 | 0.00 | 0.00 | -79 |
| MLTX-02-005-PR-1 | Material Delivery for the Site | 7 | 100% | 100% | 16-Jun-26 | 23-Jun-26 | 21-Sep-26 A | 21-Sep-26 A | 0.00 | 0.00 | 0.00 | -77 |
| **INTERLOCKING PAVING** | | 12 | 0% | 0% | 15-Jul-26 | 28-Jul-26 | 15-Sep-26 A | 15-Sep-26 A | 0.00 | 0.00 | 0.00 | -42 |
| MLTX-02-005-PR-1 | PO for Interlocking Block Pavers | 5 | 100% | 100% | 15-Jul-26 | 20-Jul-26 | 15-Sep-26 A | 15-Sep-26 A | 0.00 | 0.00 | 0.00 | -49 |
| MLTX-02-005-PR-1 | Material Delivery for Interlocking Block Pavers | 7 | 100% | 100% | 21-Jul-26 | 28-Jul-26 | 15-Sep-26 A | 15-Sep-26 A | 0.00 | 0.00 | 0.00 | -42 |
| **MARKING PAINT** | | 12 | 0% | 0% | 16-Jun-26 | 29-Jun-26 | 29-Sep-26 | 12-Oct-26 | 0.00 | 0.00 | 0.00 | -89 |
| MLTX-02-005-PR-1 | PO for Marking Paint | 5 | 100% | 0% | 16-Jun-26 | 21-Jun-26 | 29-Sep-26 | 04-Oct-26 | 0.00 | 0.00 | 0.00 | -89 |
| MLTX-02-005-PR-1 | Material Delivery for Marking Paint | 7 | 100% | 0% | 22-Jun-26 | 29-Jun-26 | 05-Oct-26 | 12-Oct-26 | 0.00 | 0.00 | 0.00 | -89 |
| **PACKAGE AC UNITS** | | 20 | 0% | 0% | 04-Jul-26 | 26-Jul-26 | 07-Jul-26 A | 07-Jul-26 A | 0.00 | 0.00 | 0.00 | 16 |
| MLTX-02-005-PR-1 | PO for Package AC Units | 5 | 100% | 100% | 04-Jul-26 | 08-Jul-26 | 07-Jul-26 A | 07-Jul-26 A | 0.00 | 0.00 | 0.00 | 1 |
| MLTX-02-005-PR-1 | Material Delivery for Package AC Units | 15 | 100% | 100% | 09-Jul-26 | 26-Jul-26 | 07-Jul-26 A | 07-Jul-26 A | 0.00 | 0.00 | 0.00 | 16 |
| **AIR DIFUSSERS/GRILLS** | | 20 | 0% | 0% | 04-Jul-26 | 26-Jul-26 | 29-Sep-26 | 21-Oct-26 | 0.00 | 0.00 | 0.00 | -74 |
| MLTX-02-005-PR-1 | PO for Air Difussers/Grills | 5 | 100% | 0% | 04-Jul-26 | 08-Jul-26 | 29-Sep-26 | 04-Oct-26 | 0.00 | 0.00 | 0.00 | -74 |
| MLTX-02-005-PR-1 | Material Delivery for Air Difussers/Grills | 15 | 100% | 0% | 09-Jul-26 | 26-Jul-26 | 05-Oct-26 | 21-Oct-26 | 0.00 | 0.00 | 0.00 | -74 |
| **GALVANIZED DUCTS** | | 20 | 0% | 0% | 04-Jul-26 | 26-Jul-26 | 29-Sep-26 | 21-Oct-26 | 0.00 | 0.00 | 0.00 | -74 |
| MLTX-02-005-PR-1 | PO for Galvanized Duct | 5 | 100% | 0% | 04-Jul-26 | 08-Jul-26 | 29-Sep-26 | 04-Oct-26 | 0.00 | 0.00 | 0.00 | -74 |
| MLTX-02-005-PR-1 | Material Delivery for Galvanized Duct | 15 | 100% | 0% | 09-Jul-26 | 26-Jul-26 | 05-Oct-26 | 21-Oct-26 | 0.00 | 0.00 | 0.00 | -74 |
| **EXHAUST FANS** | | 20 | 0% | 0% | 04-Jul-26 | 26-Jul-26 | 29-Sep-26 | 21-Oct-26 | 0.00 | 0.00 | 0.00 | -74 |
| MLTX-02-005-PR-1 | PO for Exhaust Fans | 5 | 100% | 0% | 04-Jul-26 | 08-Jul-26 | 29-Sep-26 | 04-Oct-26 | 0.00 | 0.00 | 0.00 | -74 |
| MLTX-02-005-PR-1 | Material Delivery for Exhaust Fans | 15 | 100% | 0% | 09-Jul-26 | 26-Jul-26 | 05-Oct-26 | 21-Oct-26 | 0.00 | 0.00 | 0.00 | -74 |
| **DISTRIBUTION BOARDS** | | 20 | 0% | 0% | 04-Jul-26 | 26-Jul-26 | 17-Oct-26 | 08-Nov-26 | 0.00 | 0.00 | 0.00 | -89 |
| MLTX-02-005-PR-1 | PO for Distribution Boards | 5 | 100% | 0% | 04-Jul-26 | 08-Jul-26 | 17-Oct-26 | 21-Oct-26 | 0.00 | 0.00 | 0.00 | -89 |
| MLTX-02-005-PR-1 | Material Delivery for Distribution Boards | 15 | 100% | 0% | 09-Jul-26 | 26-Jul-26 | 22-Oct-26 | 08-Nov-26 | 0.00 | 0.00 | 0.00 | -89 |
| **POWER CABLES** | | 15 | 0% | 0% | 09-Jul-26 | 26-Jul-26 | 22-Oct-26 | 08-Nov-26 | 0.00 | 0.00 | 0.00 | -89 |
| MLTX-02-005-PR-1 | PO for Power Cables | 5 | 100% | 0% | 09-Jul-26 | 14-Jul-26 | 22-Oct-26 | 27-Oct-26 | 0.00 | 0.00 | 0.00 | -89 |
| MLTX-02-005-PR-1 | Material Delivery for Power Cables | 10 | 100% | 0% | 15-Jul-26 | 26-Jul-26 | 28-Oct-26 | 08-Nov-26 | 0.00 | 0.00 | 0.00 | -89 |
| **LIGHT FIXTURES** | | 40 | 0% | 0% | 15-Jul-26 | 01-Aug-26 | 07-Jul-26 A | 08-Nov-26 | 0.00 | 0.00 | 0.00 | -84 |
| MLTX-02-005-PR-1 | PO for Light Fixtures | 5 | 100% | 100% | 15-Jul-26 | 20-Jul-26 | 07-Jul-26 A | 07-Jul-26 A | 0.00 | 0.00 | 0.00 | 11 |
| MLTX-02-005-PR-1 | Material Delivery for Light Fixtures | 10 | 100% | 0% | 21-Jul-26 | 01-Aug-26 | 28-Oct-26 | 08-Nov-26 | 0.00 | 0.00 | 0.00 | -84 |
| **CCTV MATERIALS** | | 50 | 0% | 0% | 21-Jul-26 | 12-Aug-26 | 29-Sep-26 | 25-Nov-26 | 0.00 | 0.00 | 0.00 | -89 |
| MLTX-02-005-PR-1 | PO for CCTV | 5 | 100% | 0% | 21-Jul-26 | 26-Jul-26 | 29-Sep-26 | 04-Oct-26 | 0.00 | 0.00 | 0.00 | -59 |
| MLTX-02-005-PR-1 | Material Delivery for CCTV | 15 | 100% | 0% | 27-Jul-26 | 12-Aug-26 | 09-Nov-26 | 25-Nov-26 | 0.00 | 0.00 | 0.00 | -89 |
| **POWER OUTLETS/SWITCHES** | | 21 | 0% | 0% | 27-Jul-26 | 19-Aug-26 | 13-Oct-26 | 05-Nov-26 | 0.00 | 0.00 | 0.00 | -66 |
| MLTX-02-005-PR-1 | PO for Power Outlets/Switches | 6 | 100% | 0% | 27-Jul-26 | 02-Aug-26 | 13-Oct-26 | 19-Oct-26 | 0.00 | 0.00 | 0.00 | -66 |
| MLTX-02-005-PR-1 | Material Delivery for Power Outlets/Switches | 15 | 100% | 0% | 03-Aug-26 | 19-Aug-26 | 20-Oct-26 | 05-Nov-26 | 0.00 | 0.00 | 0.00 | -66 |
| **LANDSCAPE WORKS** | | 114 | 0% | 0% | 03-Aug-26 | 20-Oct-26 | 16-May-26 A | 13-Feb-27 | 0.00 | 0.00 | 0.00 | -99 |
| **INTERLOCKING PAVING** | | 21 | 0% | 0% | 03-Aug-26 | 22-Aug-26 | 26-Aug-26 A | 26-Aug-26 A | 0.00 | 0.00 | 0.00 | -4 |
| MLTX-02-005-PR-1 | PO for Interlocking Block Pavers | 5 | 100% | 100% | 03-Aug-26 | 08-Aug-26 | 26-Aug-26 A | 26-Aug-26 A | 0.00 | 0.00 | 0.00 | -16 |

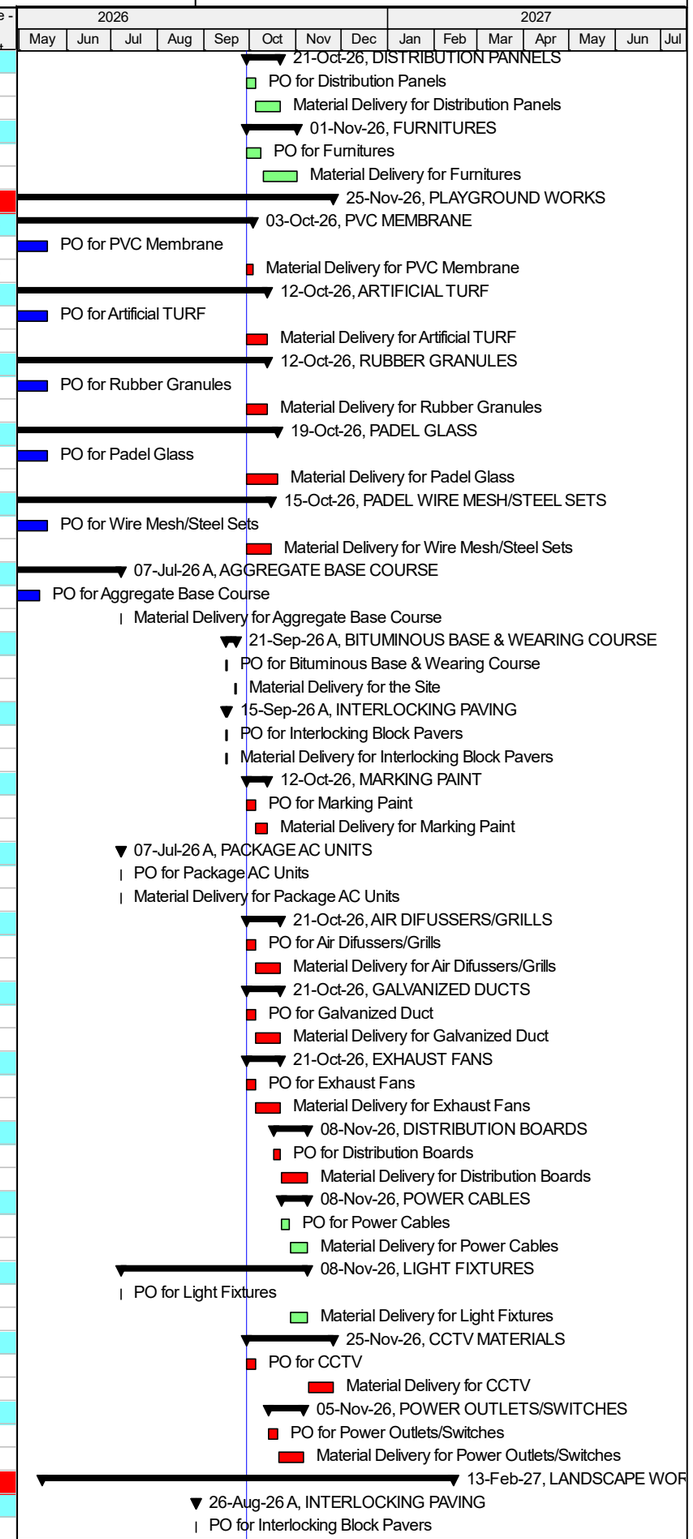


Actual Level of Effort | Actual Work | Remaining Work | Critical Remaining Work | Milestone | summary




TASK filter: All Activities

© Oracle Corporation

# MLTX-02-005 - Playground Initiative for Eastern Region (Arar-Hasa osis -Dammam)

**Updateded schedule**
**D.D 28-09-2026**

| Activity ID | Activity Name | Original Duration | Schedule % Complete | Performance % Complete | BL Project Start | BL Project Finish | Start | Finish | Planned Value Cost | Earned Value Cost | Budgeted Total Cost | Variance - BL Project |
|---|---|---|---|---|---|---|---|---|---|---|---|---|
| MLTX-02-005-PR-1 | Material Delivery for Interlocking Block Pavers | 12 | 100% | 100% | 09-Aug-26 | 22-Aug-26 | 26-Aug-26 A | 26-Aug-26 A | 0.00 | 0.00 | 0.00 | -4 |
| **CURBSTONE** | | 17 | 0% | 0% | 03-Aug-26 | 22-Aug-26 | 28-Jul-26 A | 28-Jul-26 A | 0.00 | 0.00 | 0.00 | 21 |
| MLTX-02-005-PR-1 | PO for Curbstone | 5 | 100% | 100% | 03-Aug-26 | 08-Aug-26 | 28-Jul-26 A | 28-Jul-26 A | 0.00 | 0.00 | 0.00 | 9 |
| MLTX-02-005-PR-1 | Material Delivery for Curbstone | 12 | 100% | 100% | 09-Aug-26 | 22-Aug-26 | 28-Jul-26 A | 28-Jul-26 A | 0.00 | 0.00 | 0.00 | 21 |
| **PAVEMENT MARKING** | | 15 | 0% | 0% | 03-Aug-26 | 19-Aug-26 | 20-Oct-26 | 05-Nov-26 | 0.00 | 0.00 | 0.00 | -66 |
| MLTX-02-005-PR-1 | PO for Pavement Markings | 5 | 100% | 0% | 03-Aug-26 | 08-Aug-26 | 20-Oct-26 | 25-Oct-26 | 0.00 | 0.00 | 0.00 | -66 |
| MLTX-02-005-PR-1 | Material Delivery for Pavement Markings | 10 | 100% | 0% | 09-Aug-26 | 19-Aug-26 | 26-Oct-26 | 05-Nov-26 | 0.00 | 0.00 | 0.00 | -66 |
| **TRAFFIC SIGNS** | | 14 | 0% | 0% | 04-Oct-26 | 19-Oct-26 | 26-Oct-26 | 10-Nov-26 | 0.00 | 0.00 | 0.00 | -19 |
| MLTX-02-005-PR-1 | PO for Traffic Signs | 5 | 0% | 0% | 04-Oct-26 | 08-Oct-26 | 26-Oct-26 | 31-Oct-26 | 0.00 | 0.00 | 0.00 | -19 |
| MLTX-02-005-PR-1 | Material Delivery for Traffic Signs | 9 | 0% | 0% | 10-Oct-26 | 19-Oct-26 | 01-Nov-26 | 10-Nov-26 | 0.00 | 0.00 | 0.00 | -19 |
| **IRRIGATION PIPES/SPRINKLERS** | | 16 | 0% | 0% | 09-Aug-26 | 23-Aug-26 | 17-Jun-26 A | 21-Jul-26 A | 0.00 | 0.00 | 0.00 | 28 |
| MLTX-02-005-PR-1 | PO for Irrigation Pipes/Sprinkles | 5 | 100% | 100% | 09-Aug-26 | 13-Aug-26 | 17-Jun-26 A | 17-Jun-26 A | 0.00 | 0.00 | 0.00 | 49 |
| MLTX-02-005-PR-1 | Material Delivery for Irrigation Pipes/Sprinkles | 8 | 100% | 100% | 15-Aug-26 | 23-Aug-26 | 21-Jul-26 A | 21-Jul-26 A | 0.00 | 0.00 | 0.00 | 28 |
| **AGRICULTURE SOIL** | | 17 | 0% | 0% | 21-Sep-26 | 11-Oct-26 | 21-Jan-27 | 09-Feb-27 | 0.00 | 0.00 | 0.00 | -104 |
| MLTX-02-005-PR-1 | PO for Agriculture Soil | 5 | 100% | 0% | 21-Sep-26 | 27-Sep-26 | 21-Jan-27 | 26-Jan-27 | 0.00 | 0.00 | 0.00 | -104 |
| MLTX-02-005-PR-1 | Material Delivery for Agriculture Soil | 12 | 8.33% | 0% | 28-Sep-26 | 11-Oct-26 | 27-Jan-27 | 09-Feb-27 | 0.00 | 0.00 | 0.00 | -104 |
| **TRACK SURFACE** | | 25 | 0% | 0% | 03-Sep-26 | 20-Sep-26 | 16-May-26 A | 20-Jan-27 | 0.00 | 0.00 | 0.00 | -104 |
| MLTX-02-005-PR-1 | PO for Track Surface | 5 | 100% | 100% | 03-Sep-26 | 08-Sep-26 | 16-May-26 A | 19-May-26 A | 0.00 | 0.00 | 0.00 | 93 |
| MLTX-02-005-PR-1 | Material Delivery for Track Surface | 10 | 100% | 0% | 09-Sep-26 | 20-Sep-26 | 10-Jan-27 | 20-Jan-27 | 0.00 | 0.00 | 0.00 | -104 |
| **GRASS/TREES** | | 25 | 0% | 0% | 28-Sep-26 | 20-Oct-26 | 17-May-26 A | 13-Feb-27 | 0.00 | 0.00 | 0.00 | -99 |
| MLTX-02-005-PR-1 | PO for Grass/Trees | 5 | 20% | 100% | 28-Sep-26 | 03-Oct-26 | 17-May-26 A | 20-May-26 A | 0.00 | 0.00 | 0.00 | 112 |
| MLTX-02-005-PR-1 | Material Delivery for Grass/Trees | 15 | 0% | 0% | 04-Oct-26 | 20-Oct-26 | 27-Jan-27 | 13-Feb-27 | 0.00 | 0.00 | 0.00 | -99 |
| **CABLES** | | 20 | 0% | 0% | 09-Aug-26 | 31-Aug-26 | 26-Aug-26 A | 26-Aug-26 A | 0.00 | 0.00 | 0.00 | 4 |
| MLTX-02-005-PR-1 | PO for Cables | 5 | 100% | 100% | 09-Aug-26 | 13-Aug-26 | 26-Aug-26 A | 26-Aug-26 A | 0.00 | 0.00 | 0.00 | -11 |
| MLTX-02-005-PR-1 | Material Delivery for Cables | 15 | 100% | 100% | 15-Aug-26 | 31-Aug-26 | 26-Aug-26 A | 26-Aug-26 A | 0.00 | 0.00 | 0.00 | 4 |
| **LONG LEAD ITEM** | | 93 | 0% | 0% | 20-May-26 | 04-Nov-26 | 07-Jul-26 A | 09-Jan-27 | 0.00 | 0.00 | 0.00 | -56 |
| **PLAYGROUND WORKS** | | 88 | 0% | 0% | 20-May-26 | 02-Sep-26 | 29-Sep-26 | 09-Jan-27 | 0.00 | 0.00 | 0.00 | -109 |
| **STEEL TENSION CABLES** | | 65 | 0% | 0% | 20-May-26 | 06-Aug-26 | 29-Sep-26 | 13-Dec-26 | 0.00 | 0.00 | 0.00 | -109 |
| MLTX-02-005-PR-1 | PO for Steel Tension Cables | 8 | 100% | 0% | 20-May-26 | 01-Jun-26 | 29-Sep-26 | 07-Oct-26 | 0.00 | 0.00 | 0.00 | -109 |
| MLTX-02-005-PR-1 | Material Delivery for Steel Tension Cables | 30 | 100% | 0% | 25-Jun-26 | 29-Jul-26 | 01-Nov-26 | 05-Dec-26 | 0.00 | 0.00 | 0.00 | -109 |
| MLTX-02-005-PR-1 | Material Fabrication for Steel Tension Cables | 20 | 100% | 0% | 02-Jun-26 | 24-Jun-26 | 08-Oct-26 | 31-Oct-26 | 0.00 | 0.00 | 0.00 | -109 |
| MLTX-02-005-PR-1 | Staging time | 7 | 100% | 0% | 30-Jul-26 | 06-Aug-26 | 06-Dec-26 | 13-Dec-26 | 0.00 | 0.00 | 0.00 | -109 |
| **EMERGENCY DOORS** | | 60 | 0% | 0% | 25-Jun-26 | 02-Sep-26 | 01-Nov-26 | 09-Jan-27 | 0.00 | 0.00 | 0.00 | -109 |
| MLTX-02-005-PR-1 | PO for Emergency Doors | 10 | 100% | 0% | 25-Jun-26 | 06-Jul-26 | 01-Nov-26 | 11-Nov-26 | 0.00 | 0.00 | 0.00 | -109 |
| MLTX-02-005-PR-1 | Material Delivery for Emergency Doors | 25 | 100% | 0% | 30-Jul-26 | 27-Aug-26 | 06-Dec-26 | 03-Jan-27 | 0.00 | 0.00 | 0.00 | -109 |
| MLTX-02-005-PR-1 | Material Fabrication for Emergency Doors | 20 | 100% | 0% | 07-Jul-26 | 29-Jul-26 | 12-Nov-26 | 05-Dec-26 | 0.00 | 0.00 | 0.00 | -109 |
| MLTX-02-005-PR-1 | Staging time | 5 | 100% | 0% | 29-Aug-26 | 02-Sep-26 | 04-Jan-27 | 09-Jan-27 | 0.00 | 0.00 | 0.00 | -109 |
| **PRESSURE UNITS** | | 60 | 0% | 0% | 25-Jun-26 | 02-Sep-26 | 01-Nov-26 | 09-Jan-27 | 0.00 | 0.00 | 0.00 | -109 |
| MLTX-02-005-PR-1 | PO for Pressure Units | 10 | 100% | 0% | 25-Jun-26 | 06-Jul-26 | 01-Nov-26 | 11-Nov-26 | 0.00 | 0.00 | 0.00 | -109 |
| MLTX-02-005-PR-1 | Material Delivery for Pressure Units | 25 | 100% | 0% | 30-Jul-26 | 27-Aug-26 | 06-Dec-26 | 03-Jan-27 | 0.00 | 0.00 | 0.00 | -109 |
| MLTX-02-005-PR-1 | Material Fabrication for Pressure Units | 20 | 100% | 0% | 07-Jul-26 | 29-Jul-26 | 12-Nov-26 | 05-Dec-26 | 0.00 | 0.00 | 0.00 | -109 |
| MLTX-02-005-PR-1 | Staging time | 5 | 100% | 0% | 29-Aug-26 | 02-Sep-26 | 04-Jan-27 | 09-Jan-27 | 0.00 | 0.00 | 0.00 | -109 |
| **AIR LOCK DOORS** | | 60 | 0% | 0% | 25-Jun-26 | 02-Sep-26 | 01-Nov-26 | 09-Jan-27 | 0.00 | 0.00 | 0.00 | -109 |
| MLTX-02-005-PR-1 | PO for Lock Doors | 10 | 100% | 0% | 25-Jun-26 | 06-Jul-26 | 01-Nov-26 | 11-Nov-26 | 0.00 | 0.00 | 0.00 | -109 |
| MLTX-02-005-PR-1 | Material Delivery for Lock Doors | 25 | 100% | 0% | 30-Jul-26 | 27-Aug-26 | 06-Dec-26 | 03-Jan-27 | 0.00 | 0.00 | 0.00 | -109 |
| MLTX-02-005-PR-1 | Material Fabrication for Lock Doors | 20 | 100% | 0% | 07-Jul-26 | 29-Jul-26 | 12-Nov-26 | 05-Dec-26 | 0.00 | 0.00 | 0.00 | -109 |
| MLTX-02-005-PR-1 | Staging time | 5 | 100% | 0% | 29-Aug-26 | 02-Sep-26 | 04-Jan-27 | 09-Jan-27 | 0.00 | 0.00 | 0.00 | -109 |
| **LANDSCAPE WORKS** | | 76 | 0% | 0% | 15-Aug-26 | 04-Nov-26 | 07-Jul-26 A | 20-Sep-26 A | 0.00 | 0.00 | 0.00 | 38 |
| **LIGHT POLES** | | 76 | 0% | 0% | 15-Aug-26 | 04-Nov-26 | 07-Jul-26 A | 20-Sep-26 A | 0.00 | 0.00 | 0.00 | 38 |
| MLTX-02-005-PR-1 | Staging time | 5 | 0% | 100% | 31-Oct-26 | 04-Nov-26 | 20-Sep-26 A | 20-Sep-26 A | 0.00 | 0.00 | 0.00 | 38 |
| MLTX-02-005-PR-9 | PO for Lighting poles | 10 | 100% | 100% | 15-Aug-26 | 25-Aug-26 | 07-Jul-26 A | 07-Jul-26 A | 0.00 | 0.00 | 0.00 | 42 |
| MLTX-02-005-PR-9 | Material Fabrication for Lighting poles | 30 | 93.33% | 100% | 26-Aug-26 | 30-Sep-26 | 26-Aug-26 A | 26-Aug-26 A | 0.00 | 0.00 | 0.00 | 29 |
| MLTX-02-005-PR-9 | Material Delivery for Lighting poles | 25 | 0% | 100% | 01-Oct-26 | 29-Oct-26 | 20-Sep-26 A | 20-Sep-26 A | 0.00 | 0.00 | 0.00 | 33 |
| **CONSTRUCTION PHASE** | | 226 | 45.43% | 36.64% | 29-Mar-26 | 28-Dec-26 | 04-Apr-26 A | 23-Mar-27 | 4,535,089.67 | 3,657,877.35 | 9,982,829.07 | -69 |
| **SITE WORKS** | | 226 | 38.71% | 34.47% | 29-Mar-26 | 28-Dec-26 | 04-Apr-26 A | 23-Mar-27 | 3,399,715.08 | 3,028,078.94 | 8,783,465.12 | -69 |
| **EARTH WORKS** | | 73 | 100% | 100% | 29-Mar-26 | 02-Jun-26 | 04-Apr-26 A | 08-Aug-26 A | 979,460.76 | 979,460.76 | 979,460.76 | -56 |
| MLTX-02-005-CN-118 | Excavation (in all types of soil) including Compaction | 21 | 100% | 100% | 29-Mar-26 | 21-Apr-26 | 06-Apr-26 A | 12-Apr-26 A | 182,051.70 | 182,051.70 | 182,051.70 | 9 |
| MLTX-02-005-CN-118 | Excavation (in all types of soil) including Compaction | 20 | 100% | 100% | 15-Apr-26 | 07-May-26 | 04-Apr-26 A | 02-Aug-26 A | 350,569.47 | 350,569.47 | 350,569.47 | -70 |
| MLTX-02-005-CN-119 | Excavation (in all types of soil) including Compaction | 12 | 100% | 100% | 04-May-26 | 17-May-26 | 06-Apr-26 A | 05-Aug-26 A | 139,891.20 | 139,891.20 | 139,891.20 | -66 |
| MLTX-02-005-CN-119 | Backfilling on Layers (Selected Soil) including Compaction | 20 | 100% | 100% | 22-Apr-26 | 14-May-26 | 13-Apr-26 A | 03-May-26 A | 125,667.86 | 125,667.86 | 125,667.86 | 11 |
| MLTX-02-005-CN-119 | Backfilling on Layers (Selected Soil) including Compaction | 19 | 100% | 100% | 09-May-26 | 02-Jun-26 | 06-Apr-26 A | 08-Apr-26 A | 76,629.23 | 76,629.23 | 76,629.23 | 44 |
| MLTX-02-005-CN-119 | Backfilling on Layers (Selected Soil) including Compaction | 8 | 100% | 100% | 18-May-26 | 30-May-26 | 21-Apr-26 A | 08-Aug-26 A | 104,651.30 | 104,651.30 | 104,651.30 | -59 |
| **LANDSCAPE WORKS** | | 224 | 31.25% | 25.69% | 16-May-26 | 28-Dec-26 | 16-May-26 A | 23-Mar-27 | 2,420,254.33 | 1,990,124.85 | 7,745,511.03 | -69 |
| **PLAYGROUND AREA** | | 212 | 51.19% | 74.16% | 16-May-26 | 28-Dec-26 | 18-May-26 A | 06-Mar-27 | 683,283.74 | 989,944.11 | 1,334,839.53 | -57 |

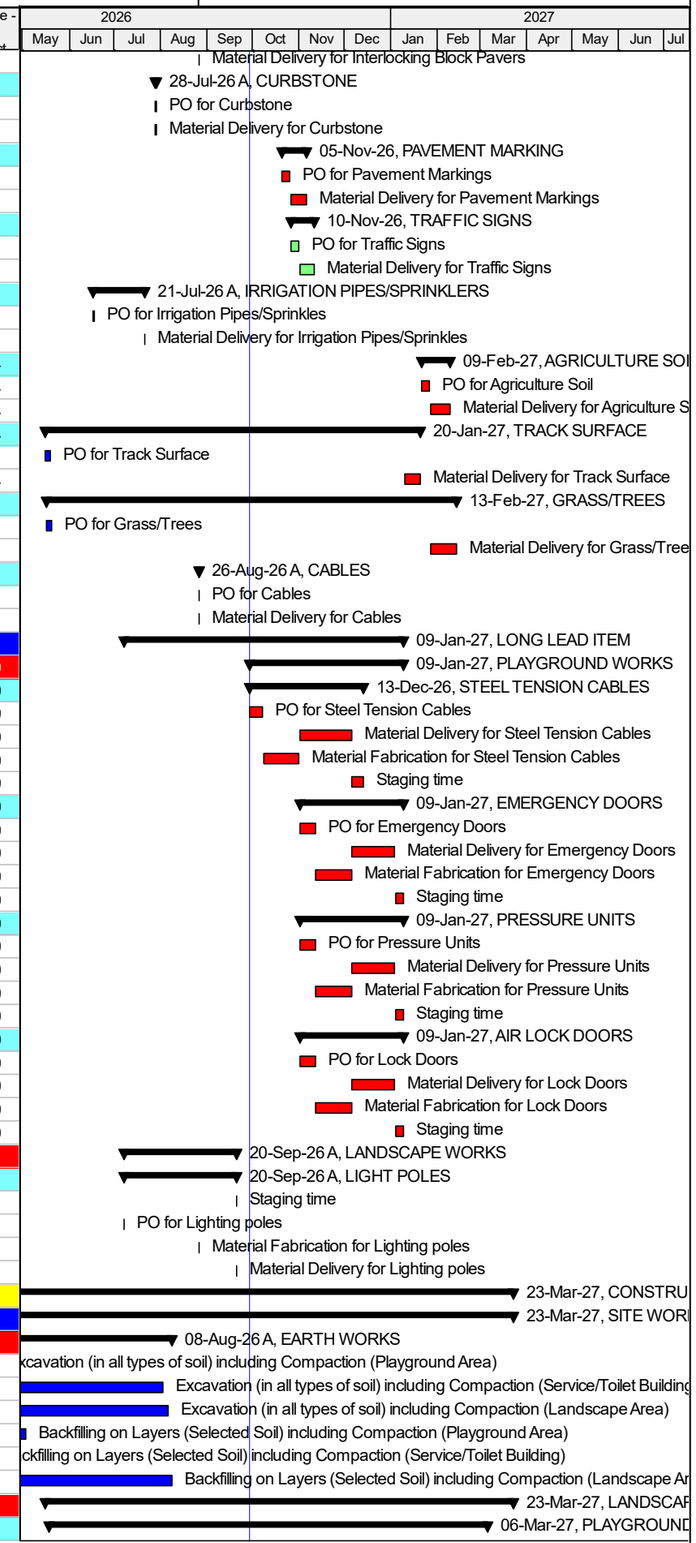


Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary




TASK filter: All Activities

© Oracle Corporation

# MLTX-02-005 - Playground Initiative for Eastern Region (Arar-Hasa osis -Dammam)

**Updateded schedule**
**D.D 28-09-2026**

| Activity ID | Activity Name | Original Duration | Schedule % Complete | Performance % Complete | BL Project Start | BL Project Finish | Start | Finish | Planned Value Cost | Earned Value Cost | Budgeted Total Cost | Variance - BL Project |
|---|---|---|---|---|---|---|---|---|---|---|---|---|
| **FOOTBALL PLAYGROUND** | | 174 | 50% | 85% | 16-May-26 | 24-Oct-26 | 18-May-26 A | 28-Nov-26 | 158,425.00 | 269,322.49 | 316,849.99 | -30 |
| MLTX-02-005-CI | Preparation and Proofing for Subgrade (Football Playground) | 20 | 100% | 100% | 16-May-26 | 10-Jun-26 | 18-May-26 A | 31-May-26 A | 79,212.50 | 79,212.50 | 79,212.50 | 9 |
| MLTX-02-005-CI | Backfilling and Compaction of Base Layers (Football | 21 | 100% | 100% | 11-Jun-26 | 05-Jul-26 | 01-Jun-26 A | 23-Jun-26 A | 15,842.50 | 15,842.50 | 15,842.50 | 10 |
| MLTX-02-005-CI | Finishing Asphalt & Concrete Surface (Football Playground) | 21 | 0% | 100% | 30-Sep-26 | 24-Oct-26 | 14-Sep-26 A | 21-Sep-26 A | 0.00 | 158,424.99 | 158,424.99 | 27 |
| MLTX-02-005-CI | Install Sport Equipments - Goal / Nets - (Football Playground) | 20 | 100% | 0% | 23-Jul-26 | 15-Aug-26 | 05-Nov-26 | 28-Nov-26 | 31,685.00 | 0.00 | 31,685.00 | -89 |
| MLTX-02-005-CI | Surface Marking and Painting (Football Playground) | 20 | 100% | 0% | 30-Jun-26 | 22-Jul-26 | 13-Oct-26 | 04-Nov-26 | 15,842.50 | 0.00 | 15,842.50 | -89 |
| MLTX-02-005-CI | Aggregate basecourse layer (Football Playground) | 21 | 100% | 100% | 06-Jul-26 | 29-Jul-26 | 24-Jun-26 A | 27-Jun-26 A | 15,842.50 | 15,842.50 | 15,842.50 | 28 |
| **PADEL PLAYGROUND** | | 191 | 45% | 70% | 11-Jun-26 | 16-Dec-26 | 18-May-26 A | 27-Dec-26 | 105,292.80 | 163,788.80 | 233,984.00 | -9 |
| MLTX-02-005-CI | Preparation and Proofing for Subgrade (Padel Playground) | 20 | 100% | 100% | 11-Jun-26 | 04-Jul-26 | 18-May-26 A | 31-May-26 A | 81,894.40 | 81,894.40 | 81,894.40 | 29 |
| MLTX-02-005-CI | Backfilling and Compaction of Base Layers (Padel | 21 | 100% | 100% | 06-Jul-26 | 29-Jul-26 | 01-Jun-26 A | 23-Jun-26 A | 11,699.20 | 11,699.20 | 11,699.20 | 31 |
| MLTX-02-005-CI | Finishing Asphalt & Concrete Surface (Padel Playground) | 21 | 0% | 100% | 25-Oct-26 | 17-Nov-26 | 30-Aug-26 A | 30-Aug-26 A | 0.00 | 58,496.00 | 58,496.00 | 67 |
| MLTX-02-005-CI | Install Sport Equipments - Goal / Nets - (Padel Playground) | 15 | 0% | 0% | 18-Nov-26 | 05-Dec-26 | 29-Nov-26 | 15-Dec-26 | 0.00 | 0.00 | 58,496.00 | -9 |
| MLTX-02-005-CI | Surface Marking and Painting (Padel Playground) | 10 | 0% | 0% | 06-Dec-26 | 16-Dec-26 | 16-Dec-26 | 27-Dec-26 | 0.00 | 0.00 | 11,699.20 | -9 |
| MLTX-02-005-CI | Aggregate basecourse layer (Padel Playground) | 21 | 100% | 100% | 30-Jul-26 | 23-Aug-26 | 23-Jun-26 A | 28-Jun-26 A | 11,699.20 | 11,699.20 | 11,699.20 | 48 |
| **BASKETBALL PLAYGROUND** | | 161 | 57.49% | 71.39% | 05-Jul-26 | 14-Dec-26 | 18-May-26 A | 06-Mar-27 | 194,800.49 | 241,875.35 | 338,831.45 | -69 |
| MLTX-02-005-CI | Preparation and Proofing for Subgrade (Basketball | 20 | 100% | 100% | 05-Jul-26 | 27-Jul-26 | 18-May-26 A | 31-May-26 A | 95,055.00 | 95,055.00 | 95,055.00 | 49 |
| MLTX-02-005-CI | Backfilling and Compaction of Base Layers (Basketball | 21 | 100% | 100% | 28-Jul-26 | 20-Aug-26 | 01-Jun-26 A | 23-Jun-26 A | 16,159.35 | 16,159.35 | 16,159.35 | 50 |
| MLTX-02-005-CI | Finishing Asphalt & Concrete Surface (Basketball | 21 | 52.38% | 100% | 15-Sep-26 | 10-Oct-26 | 29-Aug-26 A | 30-Aug-26 A | 51,782.34 | 98,857.20 | 98,857.20 | 34 |
| MLTX-02-005-CI | Install Sport Equipments - Goal / Nets - (Basketball | 15 | 0% | 0% | 15-Nov-26 | 01-Dec-26 | 16-Feb-27 | 06-Mar-27 | 0.00 | 0.00 | 80,796.75 | -80 |
| MLTX-02-005-CI | Surface Marking and Painting (Basketball Playground) | 8 | 0% | 0% | 06-Dec-26 | 14-Dec-26 | 16-Feb-27 | 25-Feb-27 | 0.00 | 0.00 | 16,159.35 | -62 |
| MLTX-02-005-CI | Aggregate basecourse layer (Basketball Playground) | 21 | 100% | 100% | 22-Aug-26 | 14-Sep-26 | 23-Jun-26 A | 28-Jun-26 A | 31,803.80 | 31,803.80 | 31,803.80 | 67 |
| **PADEL FENCE** | | 65 | 0% | 30% | 17-Dec-26 | 28-Dec-26 | 06-Aug-26 A | 31-Oct-26 | 0.00 | 24,860.73 | 82,869.08 | 50 |
| MLTX-02-005-CI | Excavation for Fence | 8 | 0% | 100% | 17-Dec-26 | 26-Dec-26 | 06-Aug-26 A | 06-Aug-26 A | 0.00 | 8,286.91 | 8,286.91 | 120 |
| MLTX-02-005-CI | Concrete Foundation for Fence including Posts Fixation | 7 | 0% | 100% | 17-Dec-26 | 24-Dec-26 | 15-Aug-26 A | 19-Aug-26 A | 0.00 | 16,573.82 | 16,573.82 | 108 |
| MLTX-02-005-CI | Backfilling and Reinstatement for Concrete Foundation | 6 | 0% | 0% | 17-Dec-26 | 23-Dec-26 | 29-Sep-26 | 05-Oct-26 | 0.00 | 0.00 | 4,143.45 | 68 |
| MLTX-02-005-CI | Tempered Glass Fenc Installation and Fixation | 10 | 0% | 0% | 17-Dec-26 | 28-Dec-26 | 20-Oct-26 | 31-Oct-26 | 0.00 | 0.00 | 33,147.63 | 50 |
| MLTX-02-005-CI | Chain Link Fence Installation and Fixation | 10 | 0% | 0% | 17-Dec-26 | 28-Dec-26 | 20-Oct-26 | 31-Oct-26 | 0.00 | 0.00 | 16,573.82 | 50 |
| MLTX-02-005-CI | Install of Fence Gates | 5 | 0% | 0% | 17-Dec-26 | 22-Dec-26 | 20-Oct-26 | 25-Oct-26 | 0.00 | 0.00 | 4,143.45 | 50 |
| **CURBSTOEN/INTERLOCK** | | 58 | 62.04% | 80.07% | 03-Sep-26 | 17-Oct-26 | 12-Aug-26 A | 22-Oct-26 | 224,765.45 | 290,096.74 | 362,305.01 | -5 |
| MLTX-02-005-CI | Interlock Installation (Grey Scale) for LandScape (Including | 21 | 23.81% | 60% | 22-Sep-26 | 17-Oct-26 | 21-Sep-26 A | 22-Oct-26 | 42,981.11 | 108,312.40 | 180,520.67 | -5 |
| MLTX-02-005-CI | Concrete Works Under Curbstone | 12 | 100% | 100% | 03-Sep-26 | 16-Sep-26 | 12-Aug-26 A | 12-Aug-26 A | 54,535.30 | 54,535.30 | 54,535.30 | 30 |
| MLTX-02-005-CI | Curbstone Installation | 4 | 100% | 100% | 17-Sep-26 | 21-Sep-26 | 12-Aug-26 A | 23-Aug-26 A | 127,249.04 | 127,249.04 | 127,249.04 | 25 |
| **AIR DOME** | | 138 | 34.25% | 11.91% | 27-Jul-26 | 09-Dec-26 | 16-May-26 A | 14-Mar-27 | 1,671,935.00 | 581,544.30 | 4,881,359.87 | -77 |
| **CIVIL WORKS** | | 81 | 28.34% | 29.58% | 30-Jul-26 | 24-Oct-26 | 16-May-26 A | 17-Nov-26 | 557,162.82 | 581,544.30 | 1,966,294.68 | -21 |
| MLTX-02-005-CI | Excavation for Foundation (Air Dome) | 15 | 100% | 100% | 30-Jul-26 | 16-Aug-26 | 16-May-26 A | 01-Jun-26 A | 127,762.34 | 127,762.34 | 127,762.34 | 65 |
| MLTX-02-005-CI | Concrete Works for Foundations including Anchor Bolts (Air | 15 | 100% | 100% | 17-Aug-26 | 02-Sep-26 | 22-Jul-26 A | 21-Sep-26 A | 168,176.84 | 168,176.84 | 168,176.84 | -16 |
| MLTX-02-005-CI | Cable System Installation (Air Dome) | 2 | 100% | 100% | 03-Sep-26 | 05-Sep-26 | 21-Sep-26 A | 21-Sep-26 A | 41,790.29 | 41,790.29 | 41,790.29 | -14 |
| MLTX-02-005-CI | Install of Membrane Covering System (Air Dome) | 21 | 0% | 0% | 30-Sep-26 | 24-Oct-26 | 04-Oct-26 | 27-Oct-26 | 0.00 | 0.00 | 936,278.81 | -3 |
| MLTX-02-005-CI | Thermal Insulation Works (Air Dome) | 10 | 0% | 0% | 30-Sep-26 | 11-Oct-26 | 07-Nov-26 | 17-Nov-26 | 0.00 | 0.00 | 448,471.57 | -32 |
| MLTX-02-005-CI | Perimeter Clamping System Installation | 10 | 90% | 100% | 17-Sep-26 | 29-Sep-26 | 21-Sep-26 A | 28-Sep-26 A | 219,433.35 | 243,814.83 | 243,814.83 | 1 |
| **MECHANICAL WORKS** | | 98 | 13.64% | 0% | 27-Jul-26 | 15-Nov-26 | 22-Oct-26 | 13-Feb-27 | 168,176.84 | 0.00 | 1,233,296.81 | -77 |
| MLTX-02-005-CI | Air Ducts and Grills Installation (Air Dome) | 20 | 0% | 0% | 12-Oct-26 | 03-Nov-26 | 10-Jan-27 | 01-Feb-27 | 0.00 | 0.00 | 728,766.30 | -77 |
| MLTX-02-005-CI | Air Units Installation (Air Dome) | 10 | 0% | 0% | 04-Nov-26 | 15-Nov-26 | 02-Feb-27 | 13-Feb-27 | 0.00 | 0.00 | 336,353.67 | -77 |
| MLTX-02-005-CI | Exhaust Fans and Ducts Installation (Air Dome) | 20 | 100% | 0% | 27-Jul-26 | 18-Aug-26 | 22-Oct-26 | 14-Nov-26 | 168,176.84 | 0.00 | 168,176.84 | -74 |
| **ELECTRICAL WORKS** | | 58 | 62.54% | 0% | 03-Sep-26 | 15-Oct-26 | 26-Nov-26 | 01-Feb-27 | 946,595.34 | 0.00 | 1,513,591.54 | -93 |
| MLTX-02-005-CI | Light Fixture Works (Air Dome) | 12 | 100% | 0% | 03-Sep-26 | 16-Sep-26 | 10-Jan-27 | 23-Jan-27 | 224,235.78 | 0.00 | 224,235.78 | -109 |
| MLTX-02-005-CI | Distribution Board and Electrical Works (Air Dome) | 14 | 42.86% | 0% | 21-Sep-26 | 07-Oct-26 | 10-Jan-27 | 25-Jan-27 | 72,075.79 | 0.00 | 168,176.84 | -94 |
| MLTX-02-005-CI | External Electrical Connection Works (Air Dome) | 20 | 30% | 0% | 21-Sep-26 | 14-Oct-26 | 10-Jan-27 | 01-Feb-27 | 50,453.05 | 0.00 | 168,176.84 | -94 |
| MLTX-02-005-CI | Emergency Generator Installation (Air Dome) | 20 | 30% | 0% | 21-Sep-26 | 14-Oct-26 | 10-Jan-27 | 01-Feb-27 | 151,359.15 | 0.00 | 504,530.51 | -94 |
| MLTX-02-005-CI | Control System Installation (Air Dome) | 21 | 28.57% | 0% | 21-Sep-26 | 15-Oct-26 | 26-Nov-26 | 20-Dec-26 | 448,471.57 | 0.00 | 448,471.57 | -56 |
| **FINISHES WORKS** | | 68 | 0% | 0% | 17-Oct-26 | 09-Dec-26 | 21-Dec-26 | 14-Mar-27 | 0.00 | 0.00 | 168,176.84 | -77 |
| MLTX-02-005-CI | Doors Installation Including Emergency, Entrance doors (Air | 21 | 0% | 0% | 17-Oct-26 | 09-Nov-26 | 21-Dec-26 | 13-Jan-27 | 0.00 | 0.00 | 112,117.89 | -56 |
| MLTX-02-005-CI | Logo and Signs Installation (Air Dome) | 21 | 0% | 0% | 16-Nov-26 | 09-Dec-26 | 14-Feb-27 | 14-Mar-27 | 0.00 | 0.00 | 56,058.95 | -77 |
| **IRRIGATION NETWORK** | | 78 | 11.73% | 80.44% | 22-Sep-26 | 17-Nov-26 | 18-Jul-26 A | 16-Feb-27 | 17,873.33 | 122,596.50 | 152,414.87 | -78 |
| MLTX-02-005-CN-1 | Installing of HDPE Pipes for Irrigation Network (Main Line) | 15 | 33.33% | 100% | 22-Sep-26 | 10-Oct-26 | 18-Jul-26 A | 20-Jul-26 A | 17,873.33 | 53,620.00 | 53,620.00 | 69 |
| MLTX-02-005-CN-1 | Installing of HDPE Pipes for Irrigation Network (Branch Lines) | 15 | 0% | 100% | 11-Oct-26 | 27-Oct-26 | 24-Aug-26 A | 01-Sep-26 A | 0.00 | 50,127.83 | 50,127.83 | 47 |
| MLTX-02-005-CN-1 | Installing of Valves and fittings for Irrigation Network | 10 | 0% | 80% | 28-Oct-26 | 08-Nov-26 | 10-Sep-26 A | 10-Oct-26 | 0.00 | 18,848.67 | 23,560.84 | 25 |
| MLTX-02-005-CN-1 | Installing of Bubblers and Spreyers | 3 | 0% | 0% | 15-Nov-26 | 17-Nov-26 | 14-Feb-27 | 16-Feb-27 | 0.00 | 0.00 | 25,106.20 | -78 |
| **NATURAL GROUND** | | 63 | 0% | 0% | 09-Nov-26 | 17-Nov-26 | 06-Dec-26 | 16-Feb-27 | 0.00 | 0.00 | 191,740.00 | -78 |
| MLTX-02-005-CN-1 | Tartan Floor Installation Works for Landscape (Including | 3 | 0% | 0% | 15-Nov-26 | 17-Nov-26 | 14-Feb-27 | 16-Feb-27 | 0.00 | 0.00 | 126,740.00 | -78 |
| MLTX-02-005-CN-1 | Compacted Natural Ground Soil Installation Works for | 5 | 0% | 0% | 09-Nov-26 | 14-Nov-26 | 06-Dec-26 | 10-Dec-26 | 0.00 | 0.00 | 65,000.00 | -23 |
| **PLANTING** | | 13 | 0% | 0% | 12-Oct-26 | 29-Oct-26 | 10-Feb-27 | 25-Feb-27 | 0.00 | 0.00 | 347,251.46 | -101 |
| MLTX-02-005-CN-1 | Placement of Sweet/Agricultural Soil (Including Levelling and | 5 | 0% | 0% | 12-Oct-26 | 17-Oct-26 | 10-Feb-27 | 15-Feb-27 | 0.00 | 0.00 | 104,175.44 | -104 |
| MLTX-02-005-CN-1 | Placement of Lawn Ground Cover (Rolling and Compaction) | 3 | 0% | 0% | 27-Oct-26 | 29-Oct-26 | 23-Feb-27 | 25-Feb-27 | 0.00 | 0.00 | 141,732.50 | -101 |

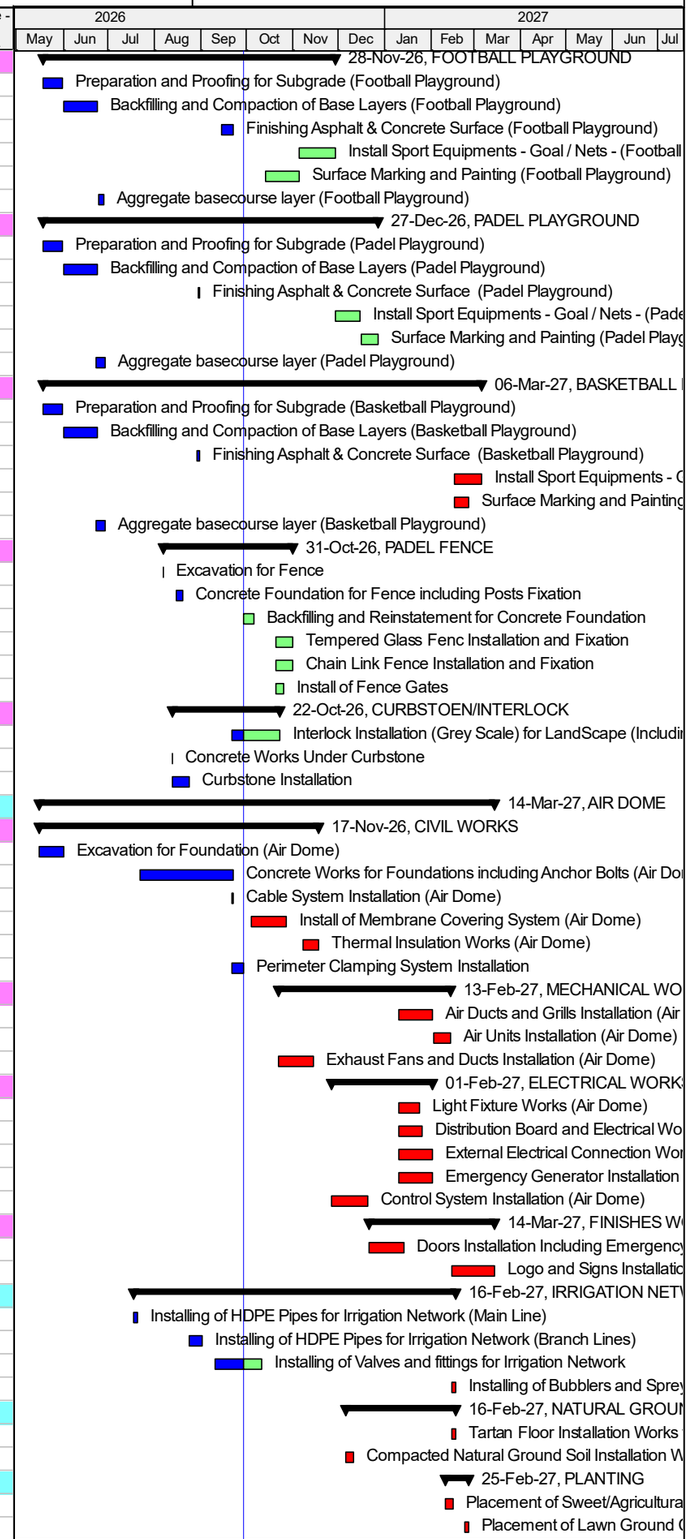


Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary




TASK filter: All Activities

© Oracle Corporation

# MLTX-02-005 - Playground Initiative for Eastern Region (Arar-Hasa osis -Dammam)

**Updateded schedule**
**D.D 28-09-2026**

| Activity ID | Activity Name | Original Duration | Schedule % Complete | Performance % Complete | BL Project Start | BL Project Finish | Start | Finish | Planned Value Cost | Earned Value Cost | Budgeted Total Cost | Variance - BL Project |
|---|---|---|---|---|---|---|---|---|---|---|---|---|
| MLTX-02-005-CN-1 | Placement and Fixation of Trees | 5 | 0% | 0% | 21-Oct-26 | 26-Oct-26 | 16-Feb-27 | 21-Feb-27 | 0.00 | 0.00 | 101,343.52 | -101 |
| **WALKING/BIKE PATHS** | | 8 | 0% | 60% | 31-Oct-26 | 08-Nov-26 | 01-Jun-26 A | 29-Sep-26 | 0.00 | 220,580.34 | 367,633.90 | 35 |
| MLTX-02-005-CN-1 | Bike Path Preparation and Installation Works | 8 | 0% | 60% | 31-Oct-26 | 08-Nov-26 | 01-Jun-26 A | 29-Sep-26 | 0.00 | 112,532.47 | 187,554.12 | 35 |
| MLTX-02-005-CN-1 | Walking Path Preparation and Installation Works | 8 | 0% | 60% | 31-Oct-26 | 08-Nov-26 | 10-Jun-26 A | 29-Sep-26 | 0.00 | 108,047.87 | 180,079.78 | 35 |
| **GENERAL/FURNITURE** | | 167 | 10.03% | 16.05% | 22-Sep-26 | 10-Dec-26 | 03-Sep-26 A | 23-Mar-27 | 47,162.25 | 75,459.60 | 470,271.40 | -84 |
| MLTX-02-005-CN-1 | Stamped Concrete Works for LandScape (Including | 8 | 0% | 0% | 09-Nov-26 | 17-Nov-26 | 29-Sep-26 | 07-Oct-26 | 0.00 | 0.00 | 93,594.00 | 35 |
| MLTX-02-005-CN-1 | Traffic Signs Posts and Poles Installation | 7 | 0% | 0% | 02-Dec-26 | 09-Dec-26 | 16-Mar-27 | 23-Mar-27 | 0.00 | 0.00 | 9,749.30 | -85 |
| MLTX-02-005-CN-1 | Fixation and Installation of Steel Frame for Benches | 8 | 0% | 0% | 09-Nov-26 | 17-Nov-26 | 29-Sep-26 | 07-Oct-26 | 0.00 | 0.00 | 17,274.79 | 35 |
| MLTX-02-005-CN-1 | Fixation and Installation of Benches | 8 | 0% | 0% | 18-Nov-26 | 26-Nov-26 | 08-Oct-26 | 17-Oct-26 | 0.00 | 0.00 | 40,307.84 | 35 |
| MLTX-02-005-CN-1 | Fixation and Installation of Precast Concrete Seats | 8 | 0% | 0% | 18-Nov-26 | 26-Nov-26 | 08-Oct-26 | 17-Oct-26 | 0.00 | 0.00 | 32,757.76 | 35 |
| MLTX-02-005-CN-1 | Fixation and Installation of Precast Concrete Seats (Circular) | 8 | 0% | 0% | 18-Nov-26 | 26-Nov-26 | 08-Oct-26 | 17-Oct-26 | 0.00 | 0.00 | 12,869.04 | 35 |
| MLTX-02-005-CN-1 | Fixation and Installation of Precast Concrete Trash Bins | 8 | 0% | 0% | 02-Dec-26 | 10-Dec-26 | 18-Oct-26 | 26-Oct-26 | 0.00 | 0.00 | 12,186.67 | 39 |
| MLTX-02-005-CN-1 | Preleminary Works for Site Light Poles Including Cable and | 8 | 62.5% | 100% | 22-Sep-26 | 01-Oct-26 | 03-Sep-26 A | 07-Sep-26 A | 47,162.25 | 75,459.60 | 75,459.60 | 20 |
| MLTX-02-005-CN-1 | Installing of Site Light Poles | 12 | 0% | 0% | 18-Nov-26 | 01-Dec-26 | 27-Feb-27 | 15-Mar-27 | 0.00 | 0.00 | 176,072.40 | -85 |
| **PARKING** | | 148 | 0% | 100% | 18-Nov-26 | 01-Dec-26 | 14-May-26 A | 19-Sep-26 A | 0.00 | 58,493.33 | 58,493.33 | 63 |
| MLTX-02-005-CN-119 | Interlock Installation (8 Cm) for Parking Area (Including | 7 | 0% | 100% | 24-Nov-26 | 01-Dec-26 | 10-Sep-26 A | 19-Sep-26 A | 0.00 | 40,945.33 | 40,945.33 | 63 |
| MLTX-02-005-CN-119 | Site Preparation & Compaction Under Interlock for Parking | 5 | 0% | 100% | 18-Nov-26 | 23-Nov-26 | 14-May-26 A | 30-Jun-26 A | 0.00 | 17,548.00 | 17,548.00 | 124 |
| **TOILET/SERVICE BUILDING** | | 135 | 94.66% | 52.51% | 03-Jun-26 | 21-Oct-26 | 24-May-26 A | 22-Dec-26 | 1,135,374.59 | 629,798.41 | 1,199,363.95 | -53 |
| **STRUCTURE WORKS** | | 78 | 100% | 100% | 03-Jun-26 | 16-Jul-26 | 24-May-26 A | 10-Aug-26 A | 194,188.64 | 194,188.64 | 194,188.64 | -21 |
| **CONCRETE WORKS** | | 71 | 100% | 100% | 20-Jun-26 | 16-Jul-26 | 25-May-26 A | 02-Jul-26 A | 134,099.30 | 134,099.30 | 134,099.30 | 12 |
| **SUB-STRUCTURE** | | 7 | 100% | 100% | 20-Jun-26 | 27-Jun-26 | 25-May-26 A | 06-Jun-26 A | 53,666.80 | 53,666.80 | 53,666.80 | 18 |
| MLTX-02-005-CN | Plain Concrete Under Footing | 2 | 100% | 100% | 20-Jun-26 | 21-Jun-26 | 25-May-26 A | 31-May-26 A | 17,106.85 | 17,106.85 | 17,106.85 | 18 |
| MLTX-02-005-CN | Reinforced Concrete Works for Slab on Grade Including | 5 | 100% | 100% | 22-Jun-26 | 27-Jun-26 | 03-Jun-26 A | 06-Jun-26 A | 36,559.95 | 36,559.95 | 36,559.95 | 18 |
| **SUPER-STRUCTURE** | | 7 | 100% | 100% | 04-Jul-26 | 16-Jul-26 | 28-Jun-26 A | 02-Jul-26 A | 80,432.50 | 80,432.50 | 80,432.50 | 12 |
| MLTX-02-005-CN | AAC Panels Works for Walls | 7 | 100% | 100% | 04-Jul-26 | 11-Jul-26 | 28-Jun-26 A | 30-Jun-26 A | 48,259.50 | 48,259.50 | 48,259.50 | 9 |
| MLTX-02-005-CN | Parpet Works and Lintels | 3 | 100% | 100% | 14-Jul-26 | 16-Jul-26 | 02-Jul-26 A | 02-Jul-26 A | 16,086.50 | 16,086.50 | 16,086.50 | 12 |
| MLTX-02-005-CN | AAC Panels Works for Slabs | 2 | 100% | 100% | 12-Jul-26 | 13-Jul-26 | 01-Jul-26 A | 01-Jul-26 A | 16,086.50 | 16,086.50 | 16,086.50 | 10 |
| **UNDER GROUND SEPTIC TANK** | | 78 | 100% | 100% | 06-Jun-26 | 07-Jul-26 | 04-Jun-26 A | 06-Jul-26 A | 49,852.54 | 49,852.54 | 49,852.54 | 1 |
| MLTX-02-005-CN-1 | Plain Concrete Under Footing | 3 | 100% | 100% | 06-Jun-26 | 08-Jun-26 | 04-Jun-26 A | 06-Jun-26 A | 17,106.85 | 17,106.85 | 17,106.85 | 2 |
| MLTX-02-005-CN-1 | Reinforced Concrete Works for Tank Slab Including | 8 | 100% | 100% | 29-Jun-26 | 07-Jul-26 | 02-Jul-26 A | 06-Jul-26 A | 8,774.37 | 8,774.37 | 8,774.37 | 1 |
| MLTX-02-005-CN-1 | Reinforced Concrete Works for Tank Foundation Including | 7 | 100% | 100% | 09-Jun-26 | 16-Jun-26 | 18-Jun-26 A | 20-Jun-26 A | 7,604.46 | 7,604.46 | 7,604.46 | -3 |
| MLTX-02-005-CN-1 | Reinforced Concrete Works for Tank Walls Including Steel | 10 | 100% | 100% | 17-Jun-26 | 28-Jun-26 | 20-Jun-26 A | 29-Jun-26 A | 16,366.86 | 16,366.86 | 16,366.86 | -1 |
| **THERMAL & MOISTER PROTECTION** | | 61 | 100% | 100% | 03-Jun-26 | 16-Jul-26 | 24-May-26 A | 10-Aug-26 A | 10,236.80 | 10,236.80 | 10,236.80 | -21 |
| **ANTI TERMIT CONTROL** | | 13 | 100% | 100% | 03-Jun-26 | 17-Jun-26 | 24-May-26 A | 03-Jun-26 A | 4,387.50 | 4,387.50 | 4,387.50 | 12 |
| MLTX-02-005-CN | Anti Termite Works Under Foundation | 1 | 100% | 100% | 03-Jun-26 | 03-Jun-26 | 31-May-26 A | 03-Jun-26 A | 1,755.00 | 1,755.00 | 1,755.00 | 0 |
| MLTX-02-005-CN | Anti Termite Works Under Slab on Grade and Grade Beams | 1 | 100% | 100% | 17-Jun-26 | 17-Jun-26 | 24-May-26 A | 25-May-26 A | 2,632.50 | 2,632.50 | 2,632.50 | 17 |
| **POLYETHYLENE SHEET** | | 13 | 100% | 100% | 04-Jun-26 | 18-Jun-26 | 25-May-26 A | 04-Jun-26 A | 2,193.30 | 2,193.30 | 2,193.30 | 12 |
| MLTX-02-005-CN | Water Proofing Under Blinding Concrete (Polythelen Sheet) | 1 | 100% | 100% | 04-Jun-26 | 04-Jun-26 | 01-Jun-26 A | 04-Jun-26 A | 877.32 | 877.32 | 877.32 | 0 |
| MLTX-02-005-CN | Water Proofing Under Slab on Grade (Polythelen Sheet) | 1 | 100% | 100% | 18-Jun-26 | 18-Jun-26 | 25-May-26 A | 31-May-26 A | 1,315.98 | 1,315.98 | 1,315.98 | 16 |
| **EPOXY** | | 6 | 100% | 100% | 08-Jul-26 | 16-Jul-26 | 11-Jul-26 A | 10-Aug-26 A | 3,656.00 | 3,656.00 | 3,656.00 | -21 |
| MLTX-02-005-CN | Surface Preparation for Epoxy Coating | 3 | 100% | 100% | 08-Jul-26 | 11-Jul-26 | 11-Jul-26 A | 11-Jul-26 A | 1,096.80 | 1,096.80 | 1,096.80 | 0 |
| MLTX-02-005-CN | Epoxy Coating for Walls and Slab of Tank | 5 | 100% | 100% | 12-Jul-26 | 16-Jul-26 | 28-Jul-26 A | 10-Aug-26 A | 2,559.20 | 2,559.20 | 2,559.20 | -21 |
| **MASONARY WORK** | | 5 | 100% | 100% | 28-Jun-26 | 02-Jul-26 | 06-Jul-26 A | 08-Jul-26 A | 12,284.10 | 12,284.10 | 12,284.10 | -4 |
| MLTX-02-005-CN-126 | CMU Masonary Works Including all Accessories | 5 | 100% | 100% | 28-Jun-26 | 02-Jul-26 | 06-Jul-26 A | 08-Jul-26 A | 12,284.10 | 12,284.10 | 12,284.10 | -4 |
| **THERMAL & MOISTER PROTECTION** | | 22 | 100% | 76.07% | 18-Jul-26 | 10-Aug-26 | 10-Sep-26 A | 07-Oct-26 | 34,698.32 | 26,394.68 | 34,698.32 | -49 |
| MLTX-02-005-CN-126 | Preparing Surface and Preliminary Works for Toilets | 2 | 100% | 100% | 18-Jul-26 | 19-Jul-26 | 10-Sep-26 A | 10-Sep-26 A | 2,105.86 | 2,105.86 | 2,105.86 | -46 |
| MLTX-02-005-CN-126 | Finalize Water Proofing Works for Toilets | 5 | 100% | 100% | 20-Jul-26 | 25-Jul-26 | 12-Sep-26 A | 12-Sep-26 A | 4,913.66 | 4,913.66 | 4,913.66 | -42 |
| MLTX-02-005-CN-126 | Preparing Surface and Preliminary Works for Roofing and | 6 | 100% | 100% | 26-Jul-26 | 01-Aug-26 | 20-Sep-26 A | 20-Sep-26 A | 11,071.52 | 11,071.52 | 11,071.52 | -43 |
| MLTX-02-005-CN-126 | Finalize Water Proofing Works for Roofing and Wet Areas | 8 | 100% | 50% | 02-Aug-26 | 10-Aug-26 | 20-Sep-26 A | 07-Oct-26 | 16,607.28 | 8,303.64 | 16,607.28 | -49 |
| **MECHANICAL WORK** | | 79 | 98.23% | 43.99% | 26-Jul-26 | 07-Oct-26 | 12-Jul-26 A | 08-Dec-26 | 259,998.07 | 116,442.91 | 264,673.10 | -53 |
| **HVAC SYSTEM** | | 42 | 100% | 47.55% | 12-Aug-26 | 14-Sep-26 | 12-Jul-26 A | 16-Nov-26 | 27,883.37 | 13,259.41 | 27,883.37 | -53 |
| MLTX-02-005-CN-1 | Preliminary HVAC and Ventilation Works | 3 | 100% | 100% | 12-Aug-26 | 15-Aug-26 | 12-Jul-26 A | 12-Jul-26 A | 9,359.69 | 9,359.69 | 9,359.69 | 29 |
| MLTX-02-005-CN-1 | Install and Finish HVAC and Ventilation Works Including Split | 4 | 100% | 0% | 10-Sep-26 | 14-Sep-26 | 12-Nov-26 | 16-Nov-26 | 14,623.96 | 0.00 | 14,623.96 | -53 |
| MLTX-02-005-CN-1 | Exhaust, Air Ducts Installation with all Accessories | 6 | 100% | 100% | 16-Aug-26 | 22-Aug-26 | 25-Aug-26 A | 29-Aug-26 A | 3,899.72 | 3,899.72 | 3,899.72 | -6 |
| **WATER SUPPLY SYSTEM** | | 71 | 98.43% | 59.01% | 28-Jul-26 | 29-Sep-26 | 21-Jul-26 A | 29-Nov-26 | 152,479.36 | 91,416.10 | 154,916.69 | -52 |
| MLTX-02-005-CN-1 | Installing of PPR Pipes and Fittings for Water Network | 6 | 100% | 100% | 28-Jul-26 | 03-Aug-26 | 21-Jul-26 A | 21-Jul-26 A | 6,921.94 | 6,921.94 | 6,921.94 | 11 |
| MLTX-02-005-CN-1 | Installing of HDPE Pipes and Valves for Water Supply | 7 | 100% | 50% | 10-Aug-26 | 17-Aug-26 | 19-Sep-26 A | 06-Oct-26 | 25,998.40 | 12,999.20 | 25,998.40 | -42 |
| MLTX-02-005-CN-1 | Installing of Booster Pump Units Including fittings and | 20 | 95% | 0% | 06-Sep-26 | 29-Sep-26 | 29-Sep-26 | 21-Oct-26 | 46,309.19 | 0.00 | 48,746.52 | -19 |
| MLTX-02-005-CN-1 | Installing of GRP Tanks | 20 | 100% | 100% | 13-Aug-26 | 05-Sep-26 | 06-Sep-26 A | 14-Sep-26 A | 64,995.36 | 64,995.36 | 64,995.36 | -8 |
| MLTX-02-005-CN-1 | Installing of Valves and Fittings | 5 | 100% | 100% | 04-Aug-26 | 09-Aug-26 | 05-Sep-26 A | 05-Sep-26 A | 6,499.60 | 6,499.60 | 6,499.60 | -23 |
| MLTX-02-005-CN-1 | Installing of Water Heater | 20 | 100% | 0% | 05-Sep-26 | 28-Sep-26 | 07-Nov-26 | 29-Nov-26 | 1,754.87 | 0.00 | 1,754.87 | -53 |
| **SEWER/DRAINAGE SYSTEM** | | 63 | 98.13% | 14.72% | 26-Jul-26 | 29-Sep-26 | 21-Jul-26 A | 30-Nov-26 | 78,428.28 | 11,767.40 | 79,923.17 | -53 |
| MLTX-02-005-CN-1 | Installing UPVC Pipes for Sewage Network | 2 | 100% | 100% | 26-Jul-26 | 27-Jul-26 | 21-Jul-26 A | 22-Jul-26 A | 11,767.40 | 11,767.40 | 11,767.40 | 4 |
| MLTX-02-005-CN-1 | Installing of Plumping Fixtures and Accessories | 5 | 100% | 0% | 18-Aug-26 | 23-Aug-26 | 20-Oct-26 | 25-Oct-26 | 10,358.68 | 0.00 | 10,358.68 | -53 |

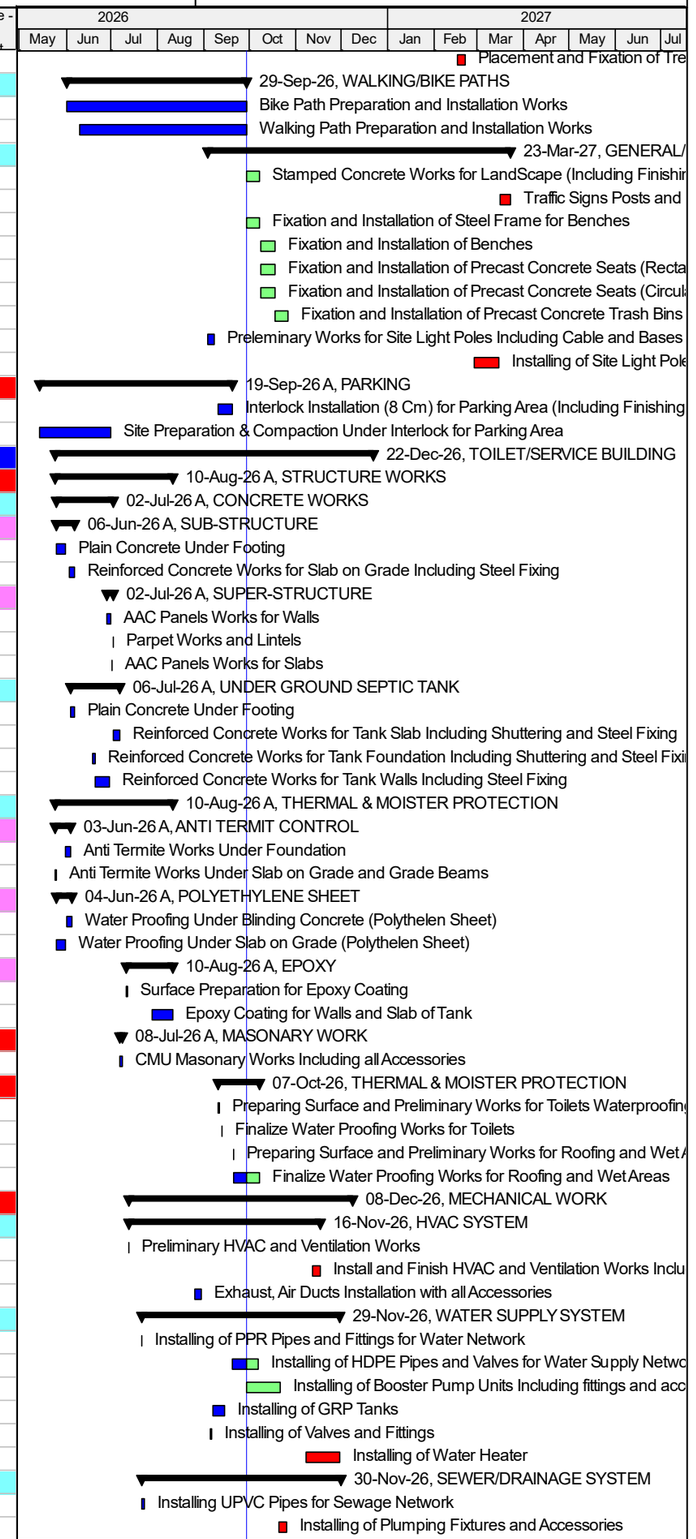


Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary



TASK filter: All Activities

© Oracle Corporation

# MLTX-02-005 - Playground Initiative for Eastern Region (Arar-Hasa osis -Dammam)


**Updateded schedule**
**D.D 28-09-2026**

PROFAST شركة برو فاست المحدودة

egis

MODON مدن

| Activity ID | Activity Name | Original Duration | Schedule % Complete | Performance % Complete | BL Project Start | BL Project Finish | Start | Finish | Planned Value Cost | Earned Value Cost | Budgeted Total Cost | Variance - BL Project |
|---|---|---|---|---|---|---|---|---|---|---|---|---|
| MLTX-02-005-CN-1 | Installing UPVC Pipes for External Connection for Sewage | 8 | 100% | 0% | 09-Aug-26 | 17-Aug-26 | 11-Oct-26 | 19-Oct-26 | 14,217.67 | 0.00 | 14,217.67 | -53 |
| MLTX-02-005-CN-1 | Installing Inspection Chamber for Sewage Network | 10 | 100% | 0% | 28-Jul-26 | 08-Aug-26 | 29-Sep-26 | 10-Oct-26 | 12,186.63 | 0.00 | 12,186.63 | -53 |
| MLTX-02-005-CN-1 | Installing of Toilet Fixtures and Accessories Such as Closets | 21 | 95.24% | 0% | 05-Sep-26 | 29-Sep-26 | 07-Nov-26 | 30-Nov-26 | 29,897.90 | 0.00 | 31,392.79 | -53 |
| **FIRE PROTECTION** | | 21 | 61.9% | 0% | 13-Sep-26 | 07-Oct-26 | 15-Nov-26 | 08-Dec-26 | 1,207.06 | 0.00 | 1,949.87 | -53 |
| MLTX-02-005-CN-1 | Installing of Fire Fighting Extinguisher and accessories | 21 | 61.9% | 0% | 13-Sep-26 | 07-Oct-26 | 15-Nov-26 | 08-Dec-26 | 1,207.06 | 0.00 | 1,949.87 | -53 |
| **ELECTRICAL WORKS** | | 116 | 84.67% | 53.29% | 18-Jul-26 | 21-Oct-26 | 14-Jul-26 A | 22-Dec-26 | 327,684.52 | 206,217.58 | 386,998.85 | -53 |
| **ROUGH-IN WORKS** | | 46 | 100% | 100% | 18-Jul-26 | 19-Jul-26 | 14-Jul-26 A | 17-Aug-26 A | 206,217.58 | 206,217.58 | 206,217.58 | -25 |
| MLTX-02-005-CN-1 | Preleminary Works for Panel Boards | 2 | 100% | 100% | 18-Jul-26 | 19-Jul-26 | 22-Jul-26 A | 09-Aug-26 A | 68,245.12 | 68,245.12 | 68,245.12 | -18 |
| MLTX-02-005-CN-1 | Preleminary Works for Cable Works | 2 | 100% | 100% | 18-Jul-26 | 19-Jul-26 | 22-Jul-26 A | 09-Aug-26 A | 12,488.95 | 12,488.95 | 12,488.95 | -17 |
| MLTX-02-005-CN-1 | Preleminary Works for Sockets and Power Points | 2 | 100% | 100% | 18-Jul-26 | 19-Jul-26 | 14-Jul-26 A | 09-Aug-26 A | 15,990.55 | 15,990.55 | 15,990.55 | -18 |
| MLTX-02-005-CN-1 | Preleminary Works for Lightning Works | 2 | 100% | 100% | 18-Jul-26 | 19-Jul-26 | 09-Aug-26 A | 17-Aug-26 A | 21,935.93 | 21,935.93 | 21,935.93 | -25 |
| MLTX-02-005-CN-1 | Preleminary Works for Data & Telecommunication System | 2 | 100% | 100% | 18-Jul-26 | 19-Jul-26 | 09-Aug-26 A | 17-Aug-26 A | 24,470.75 | 24,470.75 | 24,470.75 | -25 |
| MLTX-02-005-CN-1 | Preleminary Works for Security and Access Control System | 2 | 100% | 100% | 18-Jul-26 | 19-Jul-26 | 09-Aug-26 A | 17-Aug-26 A | 30,913.59 | 30,913.59 | 30,913.59 | -25 |
| MLTX-02-005-CN-1 | Preleminary Works for Earthing Works | 2 | 100% | 100% | 18-Jul-26 | 19-Jul-26 | 09-Aug-26 A | 17-Aug-26 A | 32,172.69 | 32,172.69 | 32,172.69 | -25 |
| **FIXTURE WORKS** | | 35 | 67.19% | 0% | 10-Sep-26 | 21-Oct-26 | 12-Nov-26 | 22-Dec-26 | 121,466.94 | 0.00 | 180,781.27 | -53 |
| MLTX-02-005-CN-1 | Installing of Fire automation and Fire Alarm System | 20 | 55% | 0% | 15-Sep-26 | 08-Oct-26 | 17-Nov-26 | 09-Dec-26 | 18,874.64 | 0.00 | 34,317.53 | -53 |
| MLTX-02-005-CN-1 | Installing and Finish Works of Panel Boards | 20 | 75% | 0% | 10-Sep-26 | 04-Oct-26 | 12-Nov-26 | 05-Dec-26 | 76,775.77 | 0.00 | 102,367.69 | -53 |
| MLTX-02-005-CN-1 | Installing and Finalize Works of Sockets and Power Points | 20 | 65% | 0% | 13-Sep-26 | 06-Oct-26 | 15-Nov-26 | 07-Dec-26 | 4,605.31 | 0.00 | 7,085.10 | -53 |
| MLTX-02-005-CN-1 | Installing and Finalize Works of Lighting Works including Light | 21 | 61.9% | 0% | 13-Sep-26 | 07-Oct-26 | 15-Nov-26 | 08-Dec-26 | 8,827.27 | 0.00 | 14,259.43 | -53 |
| MLTX-02-005-CN-1 | Installing Data and Telecommunication System with all | 20 | 0% | 0% | 29-Sep-26 | 21-Oct-26 | 30-Nov-26 | 22-Dec-26 | 0.00 | 0.00 | 6,239.59 | -53 |
| MLTX-02-005-CN-1 | Installing and Finalize Works of Security and Access Control | 20 | 75% | 0% | 10-Sep-26 | 04-Oct-26 | 12-Nov-26 | 05-Dec-26 | 5,437.57 | 0.00 | 7,250.09 | -53 |
| MLTX-02-005-CN-1 | Installing and Finalize Works of Earthing Works | 20 | 75% | 0% | 10-Sep-26 | 04-Oct-26 | 12-Nov-26 | 05-Dec-26 | 5,118.38 | 0.00 | 6,824.51 | -53 |
| MLTX-02-005-CN-1 | Installing and Finalize Works of Lightning Protection System | 20 | 75% | 0% | 10-Sep-26 | 04-Oct-26 | 12-Nov-26 | 05-Dec-26 | 1,828.00 | 0.00 | 2,437.33 | -53 |
| **DOORS/WINDOWS** | | 39 | 100% | 0% | 18-Jul-26 | 10-Sep-26 | 29-Sep-26 | 12-Nov-26 | 68,245.12 | 0.00 | 68,245.12 | -53 |
| MLTX-02-005-CN-126 | Preliminary Works For Doors | 3 | 100% | 0% | 18-Jul-26 | 20-Jul-26 | 29-Sep-26 | 01-Oct-26 | 7,799.44 | 0.00 | 7,799.44 | -62 |
| MLTX-02-005-CN-126 | Finalize Metal Doors for Toilets Building | 1 | 100% | 0% | 10-Sep-26 | 10-Sep-26 | 12-Nov-26 | 12-Nov-26 | 1,949.86 | 0.00 | 1,949.86 | -53 |
| MLTX-02-005-CN-130 | Finalize Glazzed Curtain Wall Works | 1 | 100% | 0% | 10-Sep-26 | 10-Sep-26 | 12-Nov-26 | 12-Nov-26 | 5,849.58 | 0.00 | 5,849.58 | -53 |
| MLTX-02-005-CN-131 | Preliminary Works For Windows/Curtain Wall | 2 | 100% | 0% | 18-Jul-26 | 19-Jul-26 | 29-Sep-26 | 30-Sep-26 | 52,646.24 | 0.00 | 52,646.24 | -62 |
| **METAL WORKS** | | 9 | 100% | 28.57% | 18-Jul-26 | 22-Aug-26 | 06-Sep-26 A | 19-Oct-26 | 13,649.02 | 3,899.72 | 13,649.02 | -49 |
| MLTX-02-005-CN-126 | Installation of Galvanized Steel Ladder | 4 | 100% | 0% | 13-Aug-26 | 17-Aug-26 | 11-Oct-26 | 14-Oct-26 | 5,849.58 | 0.00 | 5,849.58 | -49 |
| MLTX-02-005-CN-125 | Installation of DI Cover for Tank | 4 | 100% | 0% | 18-Jul-26 | 21-Jul-26 | 15-Oct-26 | 19-Oct-26 | 3,899.72 | 0.00 | 3,899.72 | -76 |
| MLTX-02-005-CN-125 | Installation of Galvanized Steel Roof Scupper | 4 | 100% | 100% | 18-Aug-26 | 22-Aug-26 | 06-Sep-26 A | 06-Sep-26 A | 3,899.72 | 3,899.72 | 3,899.72 | -13 |
| **FINISHING WORKS** | | 69 | 100% | 42.36% | 26-Jul-26 | 13-Sep-26 | 17-Aug-26 A | 15-Nov-26 | 166,130.97 | 70,370.78 | 166,130.97 | -53 |
| **FLOOR FINISHES** | | 41 | 100% | 69.32% | 04-Aug-26 | 13-Sep-26 | 15-Sep-26 A | 15-Nov-26 | 17,159.03 | 11,894.39 | 17,159.03 | -53 |
| MLTX-02-005-CN-1 | Creamic Tiles Floor Finish Works | 2 | 100% | 100% | 04-Aug-26 | 05-Aug-26 | 15-Sep-26 A | 16-Sep-26 A | 11,894.39 | 11,894.39 | 11,894.39 | -36 |
| MLTX-02-005-CN-1 | Granite Tiles Floor Finish Works | 6 | 100% | 0% | 06-Aug-26 | 12-Aug-26 | 29-Sep-26 | 05-Oct-26 | 2,924.82 | 0.00 | 2,924.82 | -45 |
| MLTX-02-005-CN-1 | Epoxy Coat on Concrete Floor | 3 | 100% | 0% | 10-Sep-26 | 13-Sep-26 | 12-Nov-26 | 15-Nov-26 | 1,169.94 | 0.00 | 1,169.94 | -53 |
| MLTX-02-005-CN-1 | Ceramic Skirting Tiles Finish Works | 4 | 100% | 0% | 13-Aug-26 | 17-Aug-26 | 06-Oct-26 | 10-Oct-26 | 1,169.88 | 0.00 | 1,169.88 | -45 |
| **WALL FINISHES** | | 68 | 100% | 43.64% | 26-Jul-26 | 12-Sep-26 | 17-Aug-26 A | 14-Nov-26 | 134,001.04 | 58,476.39 | 134,001.04 | -53 |
| MLTX-02-005-CN-1 | Preliminary Works for Wall Finish Works including Plastering | 3 | 100% | 100% | 26-Jul-26 | 28-Jul-26 | 17-Aug-26 A | 19-Aug-26 A | 18,315.62 | 18,315.62 | 18,315.62 | -19 |
| MLTX-02-005-CN-1 | Preliminary Works for Wall Finish Works (External) | 6 | 100% | 100% | 26-Jul-26 | 01-Aug-26 | 19-Aug-26 A | 31-Aug-26 A | 6,551.63 | 6,551.63 | 6,551.63 | -26 |
| MLTX-02-005-CN-1 | Painting Finish Works for External Walls | 3 | 100% | 50% | 18-Aug-26 | 20-Aug-26 | 27-Sep-26 A | 01-Oct-26 | 35,825.58 | 17,912.79 | 35,825.58 | -35 |
| MLTX-02-005-CN-1 | Ceramic Finish Works for Walls | 5 | 100% | 100% | 06-Aug-26 | 11-Aug-26 | 01-Sep-26 A | 03-Sep-26 A | 15,696.35 | 15,696.35 | 15,696.35 | -20 |
| MLTX-02-005-CN-1 | Phenolic Partitions for Toilets | 7 | 100% | 0% | 27-Aug-26 | 03-Sep-26 | 29-Oct-26 | 05-Nov-26 | 31,197.60 | 0.00 | 31,197.60 | -53 |
| MLTX-02-005-CN-1 | Stone Cladding Finish Works for External Walls | 5 | 100% | 0% | 22-Aug-26 | 26-Aug-26 | 03-Oct-26 | 07-Oct-26 | 2,275.00 | 0.00 | 2,275.00 | -35 |
| MLTX-02-005-CN-1 | Glass Partitions including all accessories and doors | 5 | 100% | 0% | 05-Sep-26 | 09-Sep-26 | 07-Nov-26 | 11-Nov-26 | 13,649.02 | 0.00 | 13,649.02 | -53 |
| MLTX-02-005-CN-1 | Granite Capping for Parpet | 2 | 100% | 0% | 11-Aug-26 | 12-Aug-26 | 08-Oct-26 | 10-Oct-26 | 8,150.24 | 0.00 | 8,150.24 | -49 |
| MLTX-02-005-CN-1 | Painting Finish Works for Internal Walls | 2 | 100% | 0% | 10-Sep-26 | 12-Sep-26 | 12-Nov-26 | 14-Nov-26 | 2,340.00 | 0.00 | 2,340.00 | -53 |
| **CELLING FINISHES** | | 8 | 100% | 0% | 11-Aug-26 | 24-Aug-26 | 29-Sep-26 | 07-Oct-26 | 14,970.90 | 0.00 | 14,970.90 | -37 |
| MLTX-02-005-CN-1 | Painting Finish Works for Ceiling | 3 | 100% | 0% | 22-Aug-26 | 24-Aug-26 | 05-Oct-26 | 07-Oct-26 | 3,427.86 | 0.00 | 3,427.86 | -37 |
| MLTX-02-005-CN-1 | Gypsum Board Suspended Ceiling Finish Works For Ceiling | 5 | 100% | 0% | 16-Aug-26 | 20-Aug-26 | 29-Sep-26 | 04-Oct-26 | 5,771.52 | 0.00 | 5,771.52 | -37 |
| MLTX-02-005-CN-1 | Preliminary Works for Ceiling Painting Works | 3 | 100% | 0% | 11-Aug-26 | 13-Aug-26 | 29-Sep-26 | 01-Oct-26 | 5,771.52 | 0.00 | 5,771.52 | -41 |
| **SPECIALTIES WORK** | | 24 | 100% | 0% | 24-Aug-26 | 20-Sep-26 | 26-Oct-26 | 22-Nov-26 | 58,495.83 | 0.00 | 58,495.83 | -53 |
| MLTX-02-005-CN-127 | Sanitary Fixtures and Accessories Works | 3 | 100% | 0% | 24-Aug-26 | 26-Aug-26 | 26-Oct-26 | 28-Oct-26 | 14,623.96 | 0.00 | 14,623.96 | -53 |
| MLTX-02-005-CN-127 | Installation of MODON Logo on the entrance | 7 | 100% | 0% | 13-Sep-26 | 20-Sep-26 | 15-Nov-26 | 22-Nov-26 | 19,498.61 | 0.00 | 19,498.61 | -53 |
| MLTX-02-005-CN-131 | Installation of Phenolic Locker | 2 | 100% | 0% | 05-Sep-26 | 06-Sep-26 | 07-Nov-26 | 08-Nov-26 | 24,373.26 | 0.00 | 24,373.26 | -53 |
| **TESTING & COMMISSIONING** | | 46 | 0% | 0% | 18-Nov-26 | 02-Jan-27 | 17-Feb-27 | 15-Apr-27 | 0.00 | 0.00 | 0.00 | -85 |
| MLTX-02-005-TC-11890 | Testing and Commissioning for MEP Works for Playground | 14 | 0% | 0% | 10-Dec-26 | 26-Dec-26 | 15-Mar-27 | 30-Mar-27 | 0.00 | 0.00 | 0.00 | -77 |
| MLTX-02-005-TC-11900 | Testing and Commissioning for MEP Works for Toilet/Service | 15 | 0% | 0% | 18-Nov-26 | 05-Dec-26 | 17-Feb-27 | 07-Mar-27 | 0.00 | 0.00 | 0.00 | -78 |
| MLTX-02-005-TC-11910 | Testing and Commissioning for MEP Works for Landscape | 20 | 0% | 0% | 10-Dec-26 | 02-Jan-27 | 24-Mar-27 | 15-Apr-27 | 0.00 | 0.00 | 0.00 | -85 |
| **DAMMAM** | | 245 | 48.19% | 35.08% | 03-Mar-26 | 29-Dec-26 | 04-Mar-26 A | 14-Apr-27 | 4,772,983.34 | 3,474,412.25 | 9,904,307.16 | -87 |
| **MOBILIZATION** | | 25 | 0% | 0% | 03-Mar-26 | 04-Apr-26 | 04-Mar-26 A | 04-Apr-26 A | 0.00 | 0.00 | 0.00 | 0 |
| **TOPOGRAPHIC SURVEY** | | 5 | 0% | 0% | 03-Mar-26 | 08-Mar-26 | 04-Mar-26 A | 08-Mar-26 A | 0.00 | 0.00 | 0.00 | 0 |
| MLTX-02-005-MB-2100 | Site Survey Works | 5 | 100% | 100% | 03-Mar-26 | 08-Mar-26 | 04-Mar-26 A | 08-Mar-26 A | 0.00 | 0.00 | 0.00 | 0 |

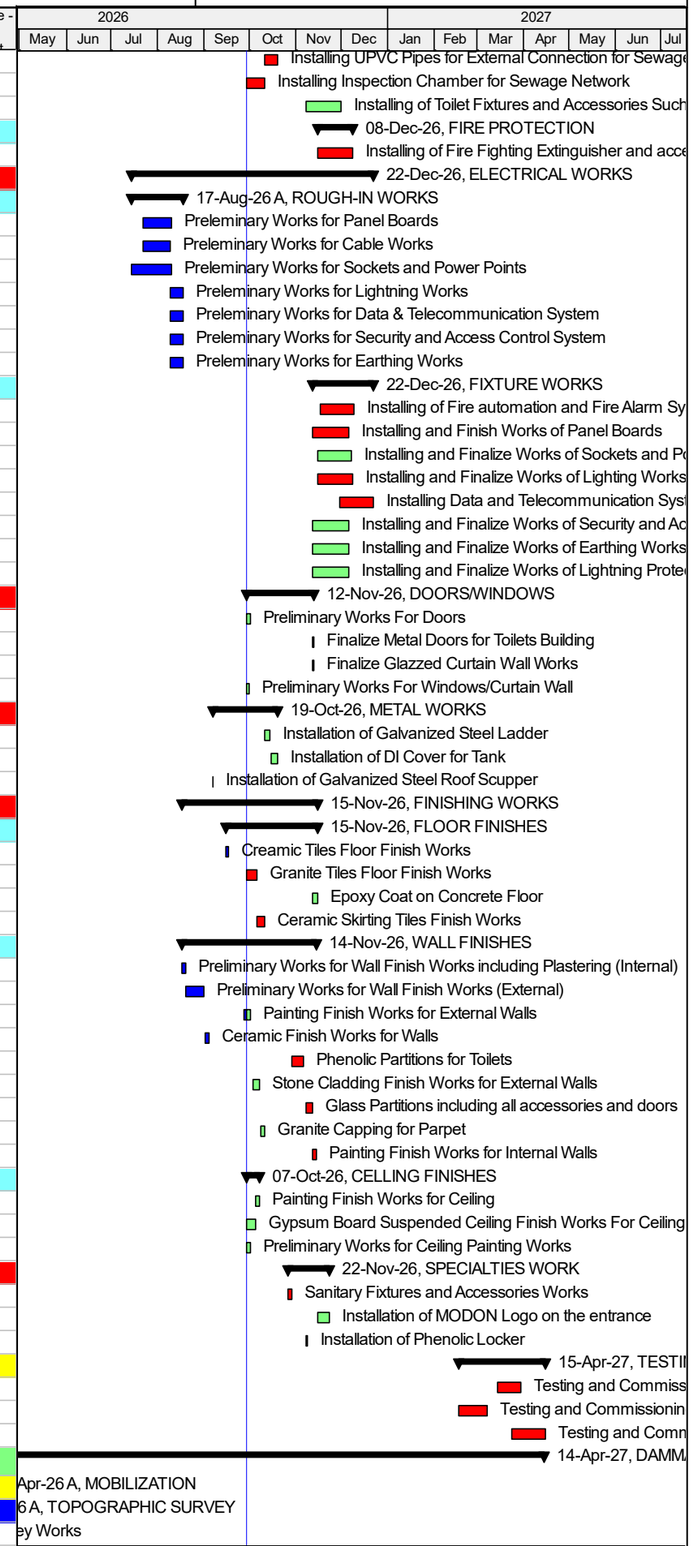


Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary




TASK filter: All Activities

© Oracle Corporation

# MLTX-02-005 - Playground Initiative for Eastern Region (Arar-Hasa osis -Dammam)

**Updateded schedule**
**D.D 28-09-2026**

| Activity ID | Activity Name | Original Duration | Schedule % Complete | Performance % Complete | BL Project Start | BL Project Finish | Start | Finish | Planned Value Cost | Earned Value Cost | Budgeted Total Cost | Variance - BL Project |
|---|---|---|---|---|---|---|---|---|---|---|---|---|
| **SITE FACILITIES & OFFICES** | | 24 | 0% | 0% | 03-Mar-26 | 02-Apr-26 | 04-Mar-26 A | 02-Apr-26 A | 0.00 | 0.00 | 0.00 | 0 |
| MLTX-02-005-MB-1980 | Manpower Mobalization | 5 | 100% | 100% | 29-Mar-26 | 02-Apr-26 | 29-Mar-26 A | 02-Apr-26 A | 0.00 | 0.00 | 0.00 | 0 |
| MLTX-02-005-MB-1990 | Equipment Mobalization | 7 | 100% | 100% | 26-Mar-26 | 02-Apr-26 | 26-Mar-26 A | 02-Apr-26 A | 0.00 | 0.00 | 0.00 | 0 |
| MLTX-02-005-MB-2010 | Site Layout Plan | 5 | 100% | 100% | 03-Mar-26 | 08-Mar-26 | 04-Mar-26 A | 08-Mar-26 A | 0.00 | 0.00 | 0.00 | 0 |
| MLTX-02-005-MB-2020 | Clear & Grub for Offices & Access Road | 3 | 100% | 100% | 09-Mar-26 | 11-Mar-26 | 09-Mar-26 A | 11-Mar-26 A | 0.00 | 0.00 | 0.00 | 0 |
| MLTX-02-005-MB-2030 | Construct Site Access Roads | 4 | 100% | 100% | 09-Mar-26 | 12-Mar-26 | 09-Mar-26 A | 12-Mar-26 A | 0.00 | 0.00 | 0.00 | 0 |
| MLTX-02-005-MB-2040 | Construct Temporary Fence | 7 | 100% | 100% | 12-Mar-26 | 19-Mar-26 | 12-Mar-26 A | 19-Mar-26 A | 0.00 | 0.00 | 0.00 | 0 |
| MLTX-02-005-MB-2050 | Construct Site Offices & Storage | 14 | 100% | 100% | 14-Mar-26 | 01-Apr-26 | 14-Mar-26 A | 01-Apr-26 A | 0.00 | 0.00 | 0.00 | 0 |
| MLTX-02-005-MB-2060 | Install Project Signs | 8 | 100% | 100% | 14-Mar-26 | 25-Mar-26 | 14-Mar-26 A | 25-Mar-26 A | 0.00 | 0.00 | 0.00 | 0 |
| MLTX-02-005-MB-2070 | Install Site Facilities | 4 | 100% | 100% | 24-Mar-26 | 28-Mar-26 | 24-Mar-26 A | 28-Mar-26 A | 0.00 | 0.00 | 0.00 | 0 |
| MLTX-02-005-MB-2080 | Electrical Works & Connections | 6 | 100% | 100% | 24-Mar-26 | 30-Mar-26 | 24-Mar-26 A | 30-Mar-26 A | 0.00 | 0.00 | 0.00 | 0 |
| MLTX-02-005-MB-2090 | Construct Parking Sheds | 6 | 100% | 100% | 24-Mar-26 | 30-Mar-26 | 24-Mar-26 A | 30-Mar-26 A | 0.00 | 0.00 | 0.00 | 0 |
| **PRELIMINARY SUBMITTALS** | | 20 | 0% | 0% | 09-Mar-26 | 04-Apr-26 | 09-Mar-26 A | 04-Apr-26 A | 0.00 | 0.00 | 0.00 | 0 |
| **PREPARATIONS & SUBMITTAL BY CONTRACTORS** | | 10 | 0% | 0% | 09-Mar-26 | 19-Mar-26 | 09-Mar-26 A | 19-Mar-26 A | 0.00 | 0.00 | 0.00 | 0 |
| MLTX-02-005-MB-200 | Preparation and Submittal of Detailed Work Order | 10 | 100% | 100% | 09-Mar-26 | 19-Mar-26 | 09-Mar-26 A | 19-Mar-26 A | 0.00 | 0.00 | 0.00 | 0 |
| MLTX-02-005-MB-211 | Preparation and Submittal of Project Execution Plan | 8 | 100% | 100% | 09-Mar-26 | 17-Mar-26 | 09-Mar-26 A | 17-Mar-26 A | 0.00 | 0.00 | 0.00 | 0 |
| MLTX-02-005-MB-212 | Submission of Contractor Project Quality Plan | 8 | 100% | 100% | 09-Mar-26 | 17-Mar-26 | 09-Mar-26 A | 17-Mar-26 A | 0.00 | 0.00 | 0.00 | 0 |
| MLTX-02-005-MB-213 | Submission of Construction Safety & Environmental | 8 | 100% | 100% | 09-Mar-26 | 17-Mar-26 | 09-Mar-26 A | 17-Mar-26 A | 0.00 | 0.00 | 0.00 | 0 |
| MLTX-02-005-MB-214 | Preparation and Submittal of Organization Chart | 8 | 100% | 100% | 09-Mar-26 | 17-Mar-26 | 09-Mar-26 A | 17-Mar-26 A | 0.00 | 0.00 | 0.00 | 0 |
| MLTX-02-005-MB-215 | Preparation and Submittal of Communication Plan | 8 | 100% | 100% | 09-Mar-26 | 17-Mar-26 | 09-Mar-26 A | 17-Mar-26 A | 0.00 | 0.00 | 0.00 | 0 |
| **APPROVALS BY EMPLOYERS** | | 12 | 0% | 0% | 18-Mar-26 | 04-Apr-26 | 18-Mar-26 A | 04-Apr-26 A | 0.00 | 0.00 | 0.00 | 0 |
| MLTX-02-005-MB-216 | Approval of Detailed Work Order Programme (Baseline) | 10 | 100% | 100% | 24-Mar-26 | 04-Apr-26 | 24-Mar-26 A | 04-Apr-26 A | 0.00 | 0.00 | 0.00 | 0 |
| MLTX-02-005-MB-217 | Approval of Project Execution Plan | 10 | 100% | 100% | 18-Mar-26 | 01-Apr-26 | 18-Mar-26 A | 01-Apr-26 A | 0.00 | 0.00 | 0.00 | 0 |
| MLTX-02-005-MB-218 | Approval of Contractor Project Quality Plan | 10 | 100% | 100% | 18-Mar-26 | 01-Apr-26 | 18-Mar-26 A | 01-Apr-26 A | 0.00 | 0.00 | 0.00 | 0 |
| MLTX-02-005-MB-219 | Approval of Construction Safety & Environmental | 10 | 100% | 100% | 18-Mar-26 | 01-Apr-26 | 18-Mar-26 A | 01-Apr-26 A | 0.00 | 0.00 | 0.00 | 0 |
| MLTX-02-005-MB-220 | Approval of Organization Chart | 10 | 100% | 100% | 18-Mar-26 | 01-Apr-26 | 18-Mar-26 A | 01-Apr-26 A | 0.00 | 0.00 | 0.00 | 0 |
| MLTX-02-005-MB-221 | Approval of Communication Plan | 10 | 100% | 100% | 18-Mar-26 | 01-Apr-26 | 18-Mar-26 A | 01-Apr-26 A | 0.00 | 0.00 | 0.00 | 0 |
| **ENGINEERING** | | 179 | 0% | 0% | 09-Mar-26 | 07-Jul-26 | 08-Mar-26 A | 28-Jan-27 | 0.00 | 0.00 | 0.00 | -175 |
| **SHOP DRAWINGS** | | 179 | 0% | 0% | 09-Mar-26 | 07-Jul-26 | 08-Mar-26 A | 28-Jan-27 | 0.00 | 0.00 | 0.00 | -175 |
| **SHOP DRAWINGS SUBMISSION** | | 95 | 0% | 0% | 09-Mar-26 | 13-Jun-26 | 08-Mar-26 A | 22-Oct-26 | 0.00 | 0.00 | 0.00 | -112 |
| **SHOP DRAWINGS SUBMITTALS FOR EARTHING WORKS** | | 40 | 0% | 0% | 09-Mar-26 | 27-Apr-26 | 09-Mar-26 A | 14-Mar-26 A | 0.00 | 0.00 | 0.00 | 35 |
| MLTX-02-005-EN-1 | Shop DWG Submittal for Layout Plan | 15 | 100% | 100% | 09-Mar-26 | 29-Mar-26 | 09-Mar-26 A | 14-Mar-26 A | 0.00 | 0.00 | 0.00 | 10 |
| MLTX-02-005-EN-1 | Shop DWG Submittal for Setting Out | 15 | 100% | 100% | 09-Mar-26 | 29-Mar-26 | 09-Mar-26 A | 14-Mar-26 A | 0.00 | 0.00 | 0.00 | 10 |
| MLTX-02-005-EN-1 | Shop DWG Submittal for Grading Layout Plan | 15 | 100% | 100% | 11-Apr-26 | 27-Apr-26 | 09-Mar-26 A | 14-Mar-26 A | 0.00 | 0.00 | 0.00 | 35 |
| MLTX-02-005-EN-1 | Shop DWG Submittal for Curb Setting Out Points | 15 | 100% | 100% | 09-Mar-26 | 29-Mar-26 | 09-Mar-26 A | 14-Mar-26 A | 0.00 | 0.00 | 0.00 | 10 |
| MLTX-02-005-EN-1 | Shop DWG Submittal for Signing & Marking Layout Plan | 15 | 100% | 100% | 09-Mar-26 | 29-Mar-26 | 09-Mar-26 A | 14-Mar-26 A | 0.00 | 0.00 | 0.00 | 10 |
| MLTX-02-005-EN-1 | Shop DWG Submittal for Standards Details | 15 | 100% | 100% | 09-Mar-26 | 29-Mar-26 | 09-Mar-26 A | 14-Mar-26 A | 0.00 | 0.00 | 0.00 | 10 |
| **SHOP DRAWING SUBMITTALS FOR SERVICE/TOILET WORKS** | | 61 | 0% | 0% | 09-Mar-26 | 13-Jun-26 | 09-Mar-26 A | 08-Jul-26 A | 0.00 | 0.00 | 0.00 | -22 |
| **ARCHITECTURE WORKS** | | 40 | 0% | 0% | 09-Mar-26 | 27-Apr-26 | 09-Mar-26 A | 14-Mar-26 A | 0.00 | 0.00 | 0.00 | 35 |
| MLTX-02-005-EN | Shop DWG Submittal for Floor Plan | 15 | 100% | 100% | 09-Mar-26 | 29-Mar-26 | 09-Mar-26 A | 14-Mar-26 A | 0.00 | 0.00 | 0.00 | 10 |
| MLTX-02-005-EN | Shop DWG Submittal for Elevations | 15 | 100% | 100% | 09-Mar-26 | 29-Mar-26 | 09-Mar-26 A | 14-Mar-26 A | 0.00 | 0.00 | 0.00 | 10 |
| MLTX-02-005-EN | Shop DWG Submittal for Sections | 15 | 100% | 100% | 11-Apr-26 | 27-Apr-26 | 09-Mar-26 A | 14-Mar-26 A | 0.00 | 0.00 | 0.00 | 35 |
| MLTX-02-005-EN | Shop DWG Submittal for Ceiling Plan | 15 | 100% | 100% | 11-Apr-26 | 27-Apr-26 | 09-Mar-26 A | 14-Mar-26 A | 0.00 | 0.00 | 0.00 | 35 |
| MLTX-02-005-EN | Shop DWG Submittal for Finishes Plan | 15 | 100% | 100% | 11-Apr-26 | 27-Apr-26 | 09-Mar-26 A | 14-Mar-26 A | 0.00 | 0.00 | 0.00 | 35 |
| MLTX-02-005-EN | Shop DWG Submittal for Toilet Details | 15 | 100% | 100% | 11-Apr-26 | 27-Apr-26 | 09-Mar-26 A | 14-Mar-26 A | 0.00 | 0.00 | 0.00 | 35 |
| MLTX-02-005-EN | Shop DWG Submittal for Doors/Windows Schedule | 15 | 100% | 100% | 11-Apr-26 | 27-Apr-26 | 09-Mar-26 A | 14-Mar-26 A | 0.00 | 0.00 | 0.00 | 35 |
| **STRUCTURE WORKS** | | 21 | 0% | 0% | 28-Apr-26 | 21-May-26 | 15-Mar-26 A | 19-Mar-26 A | 0.00 | 0.00 | 0.00 | 51 |
| MLTX-02-005-EN | Shop DWG Submittal for Foundation Plan | 15 | 100% | 100% | 28-Apr-26 | 14-May-26 | 15-Mar-26 A | 19-Mar-26 A | 0.00 | 0.00 | 0.00 | 45 |
| MLTX-02-005-EN | Shop DWG Submittal for Ground Floor Framing Plan | 21 | 100% | 100% | 28-Apr-26 | 21-May-26 | 15-Mar-26 A | 19-Mar-26 A | 0.00 | 0.00 | 0.00 | 51 |
| MLTX-02-005-EN | Shop DWG Submittal for Sections/Details | 21 | 100% | 100% | 28-Apr-26 | 21-May-26 | 15-Mar-26 A | 19-Mar-26 A | 0.00 | 0.00 | 0.00 | 51 |
| **MECHANCAL WORKS** | | 52 | 0% | 0% | 28-Apr-26 | 13-Jun-26 | 12-Mar-26 A | 08-Jul-26 A | 0.00 | 0.00 | 0.00 | -22 |
| MLTX-02-005-EN | Shop DWG Submittal for HVAC Plan | 21 | 100% | 100% | 17-May-26 | 13-Jun-26 | 08-Jul-26 A | 08-Jul-26 A | 0.00 | 0.00 | 0.00 | -22 |
| MLTX-02-005-EN | Shop DWG Submittal for Exhaust Air Plan | 21 | 100% | 100% | 28-Apr-26 | 21-May-26 | 08-Jul-26 A | 08-Jul-26 A | 0.00 | 0.00 | 0.00 | -38 |
| MLTX-02-005-EN | Shop DWG Submittal for HVAC Equipment Schedule | 21 | 100% | 100% | 28-Apr-26 | 21-May-26 | 08-Jul-26 A | 08-Jul-26 A | 0.00 | 0.00 | 0.00 | -38 |
| MLTX-02-005-EN | Shop DWG Submittal for Fire Fighting Layout | 21 | 100% | 100% | 28-Apr-26 | 21-May-26 | 08-Jul-26 A | 08-Jul-26 A | 0.00 | 0.00 | 0.00 | -38 |
| MLTX-02-005-EN | Shop DWG Submittal for Water Supply Layout | 21 | 100% | 100% | 28-Apr-26 | 21-May-26 | 12-Mar-26 A | 31-May-26 A | 0.00 | 0.00 | 0.00 | -5 |
| MLTX-02-005-EN | Shop DWG Submittal for Water Supply Details | 21 | 100% | 100% | 28-Apr-26 | 21-May-26 | 12-Mar-26 A | 31-May-26 A | 0.00 | 0.00 | 0.00 | -5 |
| MLTX-02-005-EN | Shop DWG Submittal for Drainage Layout | 21 | 100% | 100% | 28-Apr-26 | 21-May-26 | 12-Mar-26 A | 31-May-26 A | 0.00 | 0.00 | 0.00 | -5 |
| MLTX-02-005-EN | Shop DWG Submittal for Drainage Details | 21 | 100% | 100% | 28-Apr-26 | 21-May-26 | 12-Mar-26 A | 31-May-26 A | 0.00 | 0.00 | 0.00 | -5 |
| MLTX-02-005-EN | Shop DWG Submittal for Dut Routing Layout | 21 | 100% | 100% | 28-Apr-26 | 21-May-26 | 08-Jul-26 A | 08-Jul-26 A | 0.00 | 0.00 | 0.00 | -38 |
| MLTX-02-005-EN | Shop DWG Submittal for Diffusers Layout | 21 | 100% | 100% | 28-Apr-26 | 21-May-26 | 08-Jul-26 A | 08-Jul-26 A | 0.00 | 0.00 | 0.00 | -38 |
| **ELECTRICAL WORKS** | | 34 | 0% | 0% | 28-Apr-26 | 21-May-26 | 12-Mar-26 A | 04-May-26 A | 0.00 | 0.00 | 0.00 | 15 |
| MLTX-02-005-EN | Shop DWG Submittal for Lighting Layout | 21 | 100% | 100% | 28-Apr-26 | 21-May-26 | 15-Mar-26 A | 19-Mar-26 A | 0.00 | 0.00 | 0.00 | 51 |
| MLTX-02-005-EN | Shop DWG Submittal for Power Layout | 21 | 100% | 100% | 28-Apr-26 | 21-May-26 | 15-Mar-26 A | 19-Mar-26 A | 0.00 | 0.00 | 0.00 | 51 |

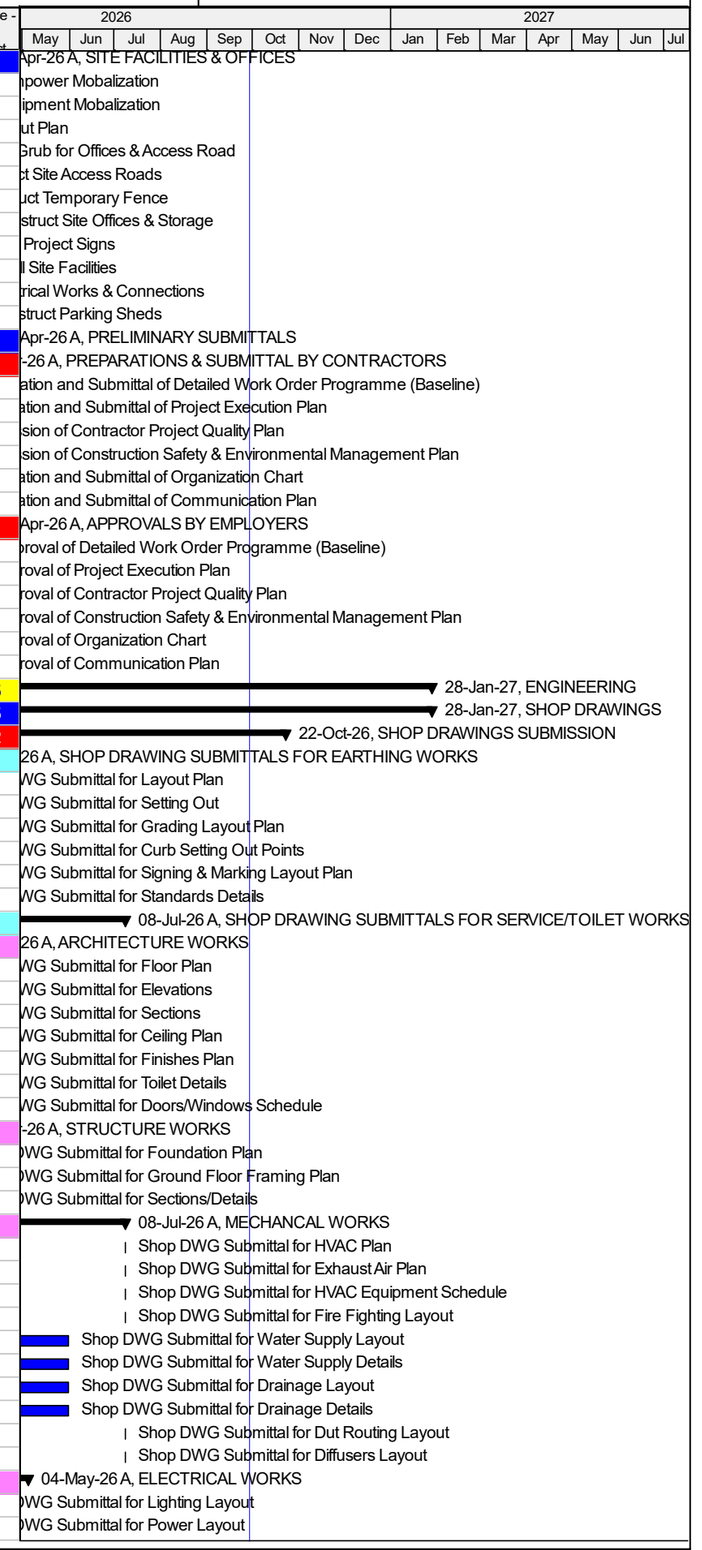


Actual Level of Effort | Actual Work | Remaining Work | Critical Remaining Work | Milestone | summary




TASK filter: All Activities

© Oracle Corporation

# MLTX-02-005 - Playground Initiative for Eastern Region (Arar-Hasa osis -Dammam)

**Updateded schedule**
**D.D 28-09-2026**

| Activity ID | Activity Name | Original Duration | Schedule % Complete | Performance % Complete | BL Project Start | BL Project Finish | Start | Finish | Planned Value Cost | Earned Value Cost | Budgeted Total Cost | Variance - BL Project |
|---|---|---|---|---|---|---|---|---|---|---|---|---|
| MLTX-02-005-EM | Shop DWG Submittal for Power Single Line Diagram | 21 | 100% | 100% | 28-Apr-26 | 21-May-26 | 12-Mar-26 A | 04-May-26 A | 0.00 | 0.00 | 0.00 | 15 |
| MLTX-02-005-EM | Shop DWG Submittal for Panel Board Schedules | 15 | 100% | 100% | 28-Apr-26 | 14-May-26 | 12-Mar-26 A | 04-May-26 A | 0.00 | 0.00 | 0.00 | 9 |
| MLTX-02-005-EM | Shop DWG Submittal for Lighting Installation Details | 21 | 100% | 100% | 28-Apr-26 | 21-May-26 | 15-Mar-26 A | 19-Mar-26 A | 0.00 | 0.00 | 0.00 | 51 |
| MLTX-02-005-EM | Shop DWG Submittal for Power Installation Details | 15 | 100% | 100% | 28-Apr-26 | 14-May-26 | 15-Mar-26 A | 19-Mar-26 A | 0.00 | 0.00 | 0.00 | 45 |
| MLTX-02-005-EM | Shop DWG Submittal for Cable Tray Installation Details | 15 | 100% | 100% | 28-Apr-26 | 14-May-26 | 12-Mar-26 A | 04-May-26 A | 0.00 | 0.00 | 0.00 | 9 |
| MLTX-02-005-EM | Shop DWG Submittal for Manhole & Ductbank Details | 15 | 100% | 100% | 28-Apr-26 | 14-May-26 | 12-Mar-26 A | 04-May-26 A | 0.00 | 0.00 | 0.00 | 9 |
| MLTX-02-005-EM | Shop DWG Submittal for Grounding Details | 15 | 100% | 100% | 28-Apr-26 | 14-May-26 | 15-Mar-26 A | 19-Mar-26 A | 0.00 | 0.00 | 0.00 | 45 |
| MLTX-02-005-EM | Shop DWG Submittal for Lightning Protection Details | 15 | 100% | 100% | 28-Apr-26 | 14-May-26 | 15-Mar-26 A | 19-Mar-26 A | 0.00 | 0.00 | 0.00 | 45 |
| MLTX-02-005-EM | Shop DWG Submittal for Fire Alarm Installation Details | 15 | 100% | 100% | 28-Apr-26 | 14-May-26 | 15-Mar-26 A | 19-Mar-26 A | 0.00 | 0.00 | 0.00 | 45 |
| MLTX-02-005-EM | Shop DWG Submittal for CCTV Details | 15 | 100% | 100% | 28-Apr-26 | 14-May-26 | 15-Mar-26 A | 19-Mar-26 A | 0.00 | 0.00 | 0.00 | 45 |
| MLTX-02-005-EM | Shop DWG Submittal for Grounding Layout | 15 | 100% | 100% | 28-Apr-26 | 14-May-26 | 15-Mar-26 A | 19-Mar-26 A | 0.00 | 0.00 | 0.00 | 45 |
| MLTX-02-005-EM | Shop DWG Submittal for Lightning Protection System Layout | 15 | 100% | 100% | 28-Apr-26 | 14-May-26 | 15-Mar-26 A | 19-Mar-26 A | 0.00 | 0.00 | 0.00 | 45 |
| MLTX-02-005-EM | Shop DWG Submittal for Fire Alarm Layout | 15 | 100% | 100% | 28-Apr-26 | 14-May-26 | 15-Mar-26 A | 19-Mar-26 A | 0.00 | 0.00 | 0.00 | 45 |
| MLTX-02-005-EM | Shop DWG Submittal for Fire Alarm Riser Diagram | 15 | 100% | 100% | 28-Apr-26 | 14-May-26 | 15-Mar-26 A | 19-Mar-26 A | 0.00 | 0.00 | 0.00 | 45 |
| MLTX-02-005-EM | Shop DWG Submittal for CCTV Layout | 15 | 100% | 100% | 28-Apr-26 | 14-May-26 | 15-Mar-26 A | 15-Mar-26 A | 0.00 | 0.00 | 0.00 | 49 |
| MLTX-02-005-EM | Shop DWG Submittal for CCTV Riser Diagram | 15 | 100% | 100% | 28-Apr-26 | 14-May-26 | 24-Mar-26 A | 04-Apr-26 A | 0.00 | 0.00 | 0.00 | 35 |
| MLTX-02-005-EM | Shop DWG Submittal for Telephone & Data Layout | 21 | 100% | 100% | 28-Apr-26 | 21-May-26 | 15-Mar-26 A | 19-Mar-26 A | 0.00 | 0.00 | 0.00 | 51 |
| MLTX-02-005-EM | Shop DWG Submittal for Telephone & Data Riser Diagram | 21 | 100% | 100% | 28-Apr-26 | 21-May-26 | 15-Mar-26 A | 19-Mar-26 A | 0.00 | 0.00 | 0.00 | 51 |
| **SHOP DRAWINGS SUBMITTALS FOR PLAYGROUND WORKS** | | 95 | 0% | 0% | 09-Mar-26 | 29-Apr-26 | 08-Mar-26 A | 22-Oct-26 | 0.00 | 0.00 | 0.00 | -147 |
| **ARCHITECTURE WORKS** | | 21 | 0% | 0% | 09-Mar-26 | 05-Apr-26 | 08-Mar-26 A | 24-May-26 A | 0.00 | 0.00 | 0.00 | -42 |
| MLTX-02-005-EM | Shop DWG Submittal for Playground Plan/Layout | 15 | 100% | 100% | 09-Mar-26 | 29-Mar-26 | 09-Mar-26 A | 14-Mar-26 A | 0.00 | 0.00 | 0.00 | 10 |
| MLTX-02-005-EM | Shop DWG Submittal for Furniture & Marking | 15 | 100% | 100% | 09-Mar-26 | 29-Mar-26 | 09-Mar-26 A | 14-Mar-26 A | 0.00 | 0.00 | 0.00 | 10 |
| MLTX-02-005-EM | Shop DWG Submittal for Sections | 15 | 100% | 100% | 09-Mar-26 | 29-Mar-26 | 09-Mar-26 A | 14-Mar-26 A | 0.00 | 0.00 | 0.00 | 10 |
| MLTX-02-005-EM | Shop DWG Submittal for Interlock Pattern Plan | 21 | 100% | 100% | 09-Mar-26 | 05-Apr-26 | 09-Mar-26 A | 14-Mar-26 A | 0.00 | 0.00 | 0.00 | 16 |
| MLTX-02-005-EM | Shop DWG Submittal for Doors/Windows Schedule | 21 | 100% | 100% | 09-Mar-26 | 05-Apr-26 | 08-Mar-26 A | 24-May-26 A | 0.00 | 0.00 | 0.00 | -42 |
| MLTX-02-005-EM | Shop DWG Submittal for Dome Internal Layout | 21 | 100% | 100% | 09-Mar-26 | 05-Apr-26 | 09-Mar-26 A | 14-Mar-26 A | 0.00 | 0.00 | 0.00 | 16 |
| **STRUCTURE WORKS** | | 21 | 0% | 0% | 06-Apr-26 | 29-Apr-26 | 14-Mar-26 A | 02-Jun-26 A | 0.00 | 0.00 | 0.00 | -26 |
| MLTX-02-005-EM | Shop DWG Submittal for Air Dome System | 21 | 100% | 100% | 06-Apr-26 | 29-Apr-26 | 14-Mar-26 A | 10-May-26 A | 0.00 | 0.00 | 0.00 | -9 |
| MLTX-02-005-EM | Shop DWG Submittal for Foundation of Air Dome | 21 | 100% | 100% | 06-Apr-26 | 29-Apr-26 | 14-Mar-26 A | 02-Jun-26 A | 0.00 | 0.00 | 0.00 | -26 |
| MLTX-02-005-EM | Shop DWG Submittal for Anchor Bolt Layout of Air Dome | 21 | 100% | 100% | 06-Apr-26 | 29-Apr-26 | 14-Mar-26 A | 02-Jun-26 A | 0.00 | 0.00 | 0.00 | -26 |
| **AIR DOME SYSTEM** | | 75 | 0% | 0% | 06-Apr-26 | 29-Apr-26 | 14-Mar-26 A | 22-Oct-26 | 0.00 | 0.00 | 0.00 | -147 |
| MLTX-02-005-EM | Shop DWG Submittal for Air Dome Structural Layout | 21 | 100% | 100% | 06-Apr-26 | 29-Apr-26 | 14-Mar-26 A | 10-May-26 A | 0.00 | 0.00 | 0.00 | -9 |
| MLTX-02-005-EM | Shop DWG Submittal for Membrane Panel Layout | 21 | 100% | 100% | 06-Apr-26 | 29-Apr-26 | 21-Jun-26 A | 21-Jun-26 A | 0.00 | 0.00 | 0.00 | -42 |
| MLTX-02-005-EM | Shop DWG Submittal for Cable Tension Layout | 21 | 100% | 0% | 06-Apr-26 | 29-Apr-26 | 29-Sep-26 | 22-Oct-26 | 0.00 | 0.00 | 0.00 | -147 |
| MLTX-02-005-EM | Shop DWG Submittal for Airlock Door Details | 21 | 100% | 0% | 06-Apr-26 | 29-Apr-26 | 29-Sep-26 | 22-Oct-26 | 0.00 | 0.00 | 0.00 | -147 |
| MLTX-02-005-EM | Shop DWG Submittal for Emergency Exit Details | 21 | 100% | 0% | 06-Apr-26 | 29-Apr-26 | 29-Sep-26 | 22-Oct-26 | 0.00 | 0.00 | 0.00 | -147 |
| **SPORTS EQUIPMENT** | | 21 | 0% | 0% | 06-Apr-26 | 29-Apr-26 | 29-Jun-26 A | 29-Jun-26 A | 0.00 | 0.00 | 0.00 | -49 |
| MLTX-02-005-EM | Shop DWG Submittal for Football Turf Installation | 21 | 100% | 100% | 06-Apr-26 | 29-Apr-26 | 29-Jun-26 A | 29-Jun-26 A | 0.00 | 0.00 | 0.00 | -49 |
| MLTX-02-005-EM | Shop DWG Submittal for Basketball Court Marking | 21 | 100% | 100% | 06-Apr-26 | 29-Apr-26 | 29-Jun-26 A | 29-Jun-26 A | 0.00 | 0.00 | 0.00 | -49 |
| MLTX-02-005-EM | Shop DWG Submittal for Padel Court Structure | 21 | 100% | 100% | 06-Apr-26 | 29-Apr-26 | 29-Jun-26 A | 29-Jun-26 A | 0.00 | 0.00 | 0.00 | -49 |
| **MECHANCAL WORKS** | | 21 | 0% | 0% | 06-Apr-26 | 29-Apr-26 | 29-Sep-26 | 22-Oct-26 | 0.00 | 0.00 | 0.00 | -147 |
| MLTX-02-005-EM | Shop DWG Submittal for HVAC Plan | 21 | 100% | 0% | 06-Apr-26 | 29-Apr-26 | 29-Sep-26 | 22-Oct-26 | 0.00 | 0.00 | 0.00 | -147 |
| MLTX-02-005-EM | Shop DWG Submittal for Exhaust Air Plan | 21 | 100% | 0% | 06-Apr-26 | 29-Apr-26 | 29-Sep-26 | 22-Oct-26 | 0.00 | 0.00 | 0.00 | -147 |
| **ELECTRICAL WORKS** | | 74 | 0% | 0% | 06-Apr-26 | 29-Apr-26 | 14-Mar-26 A | 22-Oct-26 | 0.00 | 0.00 | 0.00 | -147 |
| MLTX-02-005-EM | Shop DWG Submittal for Lighting Layout | 21 | 100% | 100% | 06-Apr-26 | 29-Apr-26 | 25-Aug-26 A | 25-Aug-26 A | 0.00 | 0.00 | 0.00 | -98 |
| MLTX-02-005-EM | Shop DWG Submittal for Power Layout | 21 | 100% | 0% | 06-Apr-26 | 29-Apr-26 | 29-Sep-26 | 22-Oct-26 | 0.00 | 0.00 | 0.00 | -147 |
| MLTX-02-005-EM | Shop DWG Submittal for Power Single Line Diagram | 21 | 100% | 0% | 06-Apr-26 | 29-Apr-26 | 29-Sep-26 | 22-Oct-26 | 0.00 | 0.00 | 0.00 | -147 |
| MLTX-02-005-EM | Shop DWG Submittal for Panel Board Schedules | 21 | 100% | 0% | 06-Apr-26 | 29-Apr-26 | 29-Sep-26 | 22-Oct-26 | 0.00 | 0.00 | 0.00 | -147 |
| MLTX-02-005-EM | Shop DWG Submittal for Power Installation Details | 21 | 100% | 0% | 06-Apr-26 | 29-Apr-26 | 29-Sep-26 | 22-Oct-26 | 0.00 | 0.00 | 0.00 | -147 |
| MLTX-02-005-EM | Shop DWG Submittal for Fire Alarm Installation Details | 21 | 100% | 100% | 06-Apr-26 | 29-Apr-26 | 25-Aug-26 A | 25-Aug-26 A | 0.00 | 0.00 | 0.00 | -98 |
| MLTX-02-005-EM | Shop DWG Submittal for CCTV Details | 21 | 100% | 100% | 06-Apr-26 | 29-Apr-26 | 25-Aug-26 A | 25-Aug-26 A | 0.00 | 0.00 | 0.00 | -98 |
| MLTX-02-005-EM | Shop DWG Submittal for Fire Alarm Layout | 21 | 100% | 100% | 06-Apr-26 | 29-Apr-26 | 14-Mar-26 A | 04-May-26 A | 0.00 | 0.00 | 0.00 | -4 |
| MLTX-02-005-EM | Shop DWG Submittal for Fire Alarm Riser Diagram | 21 | 100% | 100% | 06-Apr-26 | 29-Apr-26 | 14-Mar-26 A | 04-May-26 A | 0.00 | 0.00 | 0.00 | -4 |
| MLTX-02-005-EM | Shop DWG Submittal for CCTV Layout | 21 | 100% | 100% | 06-Apr-26 | 29-Apr-26 | 25-Aug-26 A | 25-Aug-26 A | 0.00 | 0.00 | 0.00 | -98 |
| MLTX-02-005-EM | Shop DWG Submittal for CCTV Riser Diagram | 21 | 100% | 100% | 06-Apr-26 | 29-Apr-26 | 25-Aug-26 A | 25-Aug-26 A | 0.00 | 0.00 | 0.00 | -98 |
| **SHOP DRAWINGS SUBMITTALS FOR LANDSCAPE WORKS** | | 57 | 0% | 0% | 09-Mar-26 | 15-Apr-26 | 08-Mar-26 A | 30-Jul-26 A | 0.00 | 0.00 | 0.00 | -88 |
| **ARCHITECTURE WORKS** | | 30 | 0% | 0% | 09-Mar-26 | 15-Apr-26 | 09-Mar-26 A | 19-Mar-26 A | 0.00 | 0.00 | 0.00 | 20 |
| MLTX-02-005-EM | Shop DWG Submittal for Landscape Layout | 21 | 100% | 100% | 09-Mar-26 | 05-Apr-26 | 09-Mar-26 A | 14-Mar-26 A | 0.00 | 0.00 | 0.00 | 16 |
| MLTX-02-005-EM | Shop DWG Submittal for Hardscape Plan | 21 | 100% | 100% | 09-Mar-26 | 05-Apr-26 | 09-Mar-26 A | 14-Mar-26 A | 0.00 | 0.00 | 0.00 | 16 |
| MLTX-02-005-EM | Shop DWG Submittal for Planting Plan | 15 | 100% | 100% | 30-Mar-26 | 15-Apr-26 | 15-Mar-26 A | 19-Mar-26 A | 0.00 | 0.00 | 0.00 | 20 |
| MLTX-02-005-EM | Shop DWG Submittal for Landscape Details | 15 | 100% | 100% | 09-Mar-26 | 29-Mar-26 | 09-Mar-26 A | 14-Mar-26 A | 0.00 | 0.00 | 0.00 | 10 |
| **MECHANCAL WORKS** | | 21 | 0% | 0% | 09-Mar-26 | 05-Apr-26 | 08-Mar-26 A | 04-Jun-26 A | 0.00 | 0.00 | 0.00 | -49 |
| MLTX-02-005-EM | Shop DWG Submittal for Irrigation Details | 21 | 100% | 100% | 09-Mar-26 | 05-Apr-26 | 08-Mar-26 A | 04-Jun-26 A | 0.00 | 0.00 | 0.00 | -49 |
| MLTX-02-005-EM | Shop DWG Submittal for Irrigation Layout | 21 | 100% | 100% | 09-Mar-26 | 05-Apr-26 | 08-Mar-26 A | 04-Jun-26 A | 0.00 | 0.00 | 0.00 | -49 |

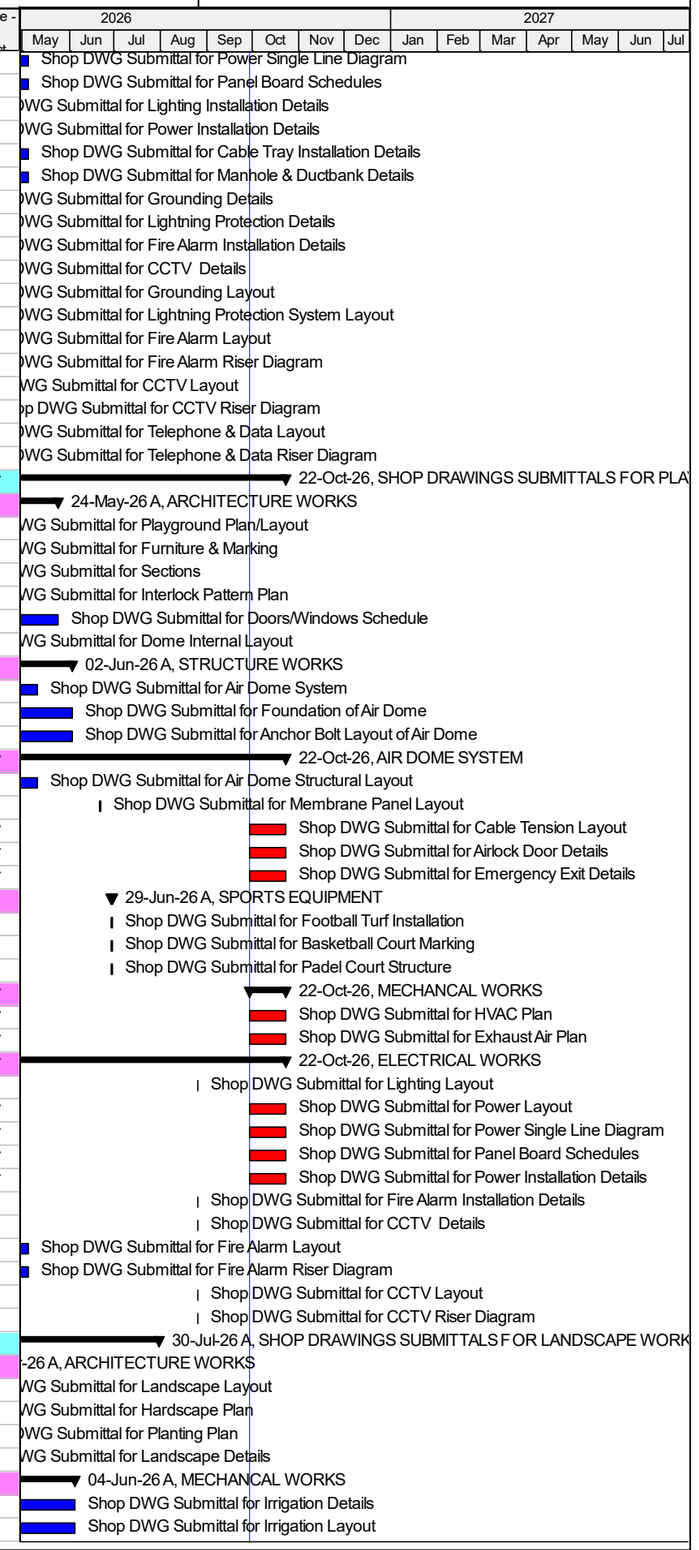





© Oracle Corporation

# MLTX-02-005 - Playground Initiative for Eastern Region (Arar-Hasa osis -Dammam)

**Updateded schedule**
**D.D 28-09-2026**

| Activity ID | Activity Name | Original Duration | Schedule % Complete | Performance % Complete | BL Project Start | BL Project Finish | Start | Finish | Planned Value Cost | Earned Value Cost | Budgeted Total Cost | Variance - BL Project |
|---|---|---|---|---|---|---|---|---|---|---|---|---|
| **ELECTRICAL WORKS** | | 30 | 0% | 0% | 09-Mar-26 | 15-Apr-26 | 30-Jul-26 A | 30-Jul-26 A | 0.00 | 0.00 | 0.00 | -88 |
| MLTX-02-005-EN | Shop DWG Submittal for Lighting General Arrangement | 30 | 100% | 100% | 09-Mar-26 | 15-Apr-26 | 30-Jul-26 A | 30-Jul-26 A | 0.00 | 0.00 | 0.00 | -88 |
| MLTX-02-005-EN | Shop DWG Submittal for Lighting Network Layout | 30 | 100% | 100% | 09-Mar-26 | 15-Apr-26 | 30-Jul-26 A | 30-Jul-26 A | 0.00 | 0.00 | 0.00 | -88 |
| MLTX-02-005-EN | Shop DWG Submittal for Lighting Details | 30 | 100% | 100% | 09-Mar-26 | 15-Apr-26 | 30-Jul-26 A | 30-Jul-26 A | 0.00 | 0.00 | 0.00 | -88 |
| MLTX-02-005-EN | Shop DWG Submittal for Lighting Single Line Diagram | 30 | 100% | 100% | 09-Mar-26 | 15-Apr-26 | 30-Jul-26 A | 30-Jul-26 A | 0.00 | 0.00 | 0.00 | -88 |
| **SHOP DRAWINGS APPROVALS** | | 164 | 0% | 0% | 30-Mar-26 | 07-Jul-26 | 14-Mar-26 A | 28-Jan-27 | 0.00 | 0.00 | 0.00 | -175 |
| **SHOP DRAWING APPROVAL FOR EARTHING WORKS** | | 41 | 0% | 0% | 30-Mar-26 | 16-May-26 | 15-Mar-26 A | 29-Mar-26 A | 0.00 | 0.00 | 0.00 | 41 |
| MLTX-02-005-EN-1 | Shop DWG Approval for Layout Plan | 21 | 100% | 100% | 30-Mar-26 | 22-Apr-26 | 15-Mar-26 A | 29-Mar-26 A | 0.00 | 0.00 | 0.00 | 21 |
| MLTX-02-005-EN-1 | Shop DWG Approval for Setting Out | 10 | 100% | 100% | 30-Mar-26 | 09-Apr-26 | 15-Mar-26 A | 29-Mar-26 A | 0.00 | 0.00 | 0.00 | 10 |
| MLTX-02-005-EN-1 | Shop DWG Approval for Grading Layout Plan | 16 | 100% | 100% | 28-Apr-26 | 16-May-26 | 15-Mar-26 A | 29-Mar-26 A | 0.00 | 0.00 | 0.00 | 41 |
| MLTX-02-005-EN-1 | Shop DWG Approval for Curb Setting Out Points | 21 | 100% | 100% | 30-Mar-26 | 22-Apr-26 | 15-Mar-26 A | 29-Mar-26 A | 0.00 | 0.00 | 0.00 | 21 |
| MLTX-02-005-EN-1 | Shop DWG Approval for Signing & Marking Layout Plan | 10 | 100% | 100% | 30-Mar-26 | 09-Apr-26 | 15-Mar-26 A | 29-Mar-26 A | 0.00 | 0.00 | 0.00 | 10 |
| MLTX-02-005-EN-1 | Shop DWG Approval for Standards Details | 15 | 100% | 100% | 30-Mar-26 | 15-Apr-26 | 15-Mar-26 A | 29-Mar-26 A | 0.00 | 0.00 | 0.00 | 15 |
| **SHOP DRAWING APPROVAL FOR SERVICE/TOILET WORKS** | | 67 | 0% | 0% | 30-Mar-26 | 07-Jul-26 | 15-Mar-26 A | 28-Jul-26 A | 0.00 | 0.00 | 0.00 | -18 |
| **ARCHITECTURE WORKS** | | 55 | 0% | 0% | 30-Mar-26 | 04-Jun-26 | 15-Mar-26 A | 29-Mar-26 A | 0.00 | 0.00 | 0.00 | 55 |
| MLTX-02-005-EN | Shop DWG Approval for Floor Plan | 30 | 100% | 100% | 30-Mar-26 | 03-May-26 | 15-Mar-26 A | 29-Mar-26 A | 0.00 | 0.00 | 0.00 | 30 |
| MLTX-02-005-EN | Shop DWG Approval for Elevations | 30 | 100% | 100% | 30-Mar-26 | 03-May-26 | 15-Mar-26 A | 29-Mar-26 A | 0.00 | 0.00 | 0.00 | 30 |
| MLTX-02-005-EN | Shop DWG Approval for Sections | 30 | 100% | 100% | 28-Apr-26 | 04-Jun-26 | 15-Mar-26 A | 29-Mar-26 A | 0.00 | 0.00 | 0.00 | 55 |
| MLTX-02-005-EN | Shop DWG Approval for Ceiling Plan | 30 | 100% | 100% | 28-Apr-26 | 04-Jun-26 | 15-Mar-26 A | 29-Mar-26 A | 0.00 | 0.00 | 0.00 | 55 |
| MLTX-02-005-EN | Shop DWG Approval for Finishes Plan | 30 | 100% | 100% | 28-Apr-26 | 04-Jun-26 | 15-Mar-26 A | 29-Mar-26 A | 0.00 | 0.00 | 0.00 | 55 |
| MLTX-02-005-EN | Shop DWG Approval for Toilet Details | 30 | 100% | 100% | 28-Apr-26 | 04-Jun-26 | 15-Mar-26 A | 29-Mar-26 A | 0.00 | 0.00 | 0.00 | 55 |
| MLTX-02-005-EN | Shop DWG Approval for Doors/Windows Schedule | 30 | 100% | 100% | 28-Apr-26 | 04-Jun-26 | 15-Mar-26 A | 29-Mar-26 A | 0.00 | 0.00 | 0.00 | 55 |
| **STRUCTURE WORKS** | | 27 | 0% | 0% | 16-May-26 | 18-Jun-26 | 24-Mar-26 A | 04-Apr-26 A | 0.00 | 0.00 | 0.00 | 62 |
| MLTX-02-005-EN | Shop DWG Approval for Foundation Plan | 15 | 100% | 100% | 16-May-26 | 04-Jun-26 | 24-Mar-26 A | 04-Apr-26 A | 0.00 | 0.00 | 0.00 | 50 |
| MLTX-02-005-EN | Shop DWG Approval for Ground Floor Framing Plan | 21 | 100% | 100% | 23-May-26 | 18-Jun-26 | 24-Mar-26 A | 04-Apr-26 A | 0.00 | 0.00 | 0.00 | 62 |
| MLTX-02-005-EN | Shop DWG Approval for Sections/Details | 21 | 100% | 100% | 23-May-26 | 18-Jun-26 | 24-Mar-26 A | 04-Apr-26 A | 0.00 | 0.00 | 0.00 | 62 |
| **MECHANCAL WORKS** | | 52 | 0% | 0% | 23-May-26 | 07-Jul-26 | 18-Mar-26 A | 11-Jul-26 A | 0.00 | 0.00 | 0.00 | -3 |
| MLTX-02-005-EN | Shop DWG Approval for HVAC Plan | 21 | 100% | 100% | 14-Jun-26 | 07-Jul-26 | 11-Jul-26 A | 11-Jul-26 A | 0.00 | 0.00 | 0.00 | -3 |
| MLTX-02-005-EN | Shop DWG Approval for Exhaust Air Plan | 21 | 100% | 100% | 23-May-26 | 18-Jun-26 | 11-Jul-26 A | 11-Jul-26 A | 0.00 | 0.00 | 0.00 | -19 |
| MLTX-02-005-EN | Shop DWG Approval for HVAC Equipment Schedule | 21 | 100% | 100% | 23-May-26 | 18-Jun-26 | 11-Jul-26 A | 11-Jul-26 A | 0.00 | 0.00 | 0.00 | -19 |
| MLTX-02-005-EN | Shop DWG Approval for Fire Fighting Layout | 21 | 100% | 100% | 23-May-26 | 18-Jun-26 | 11-Jul-26 A | 11-Jul-26 A | 0.00 | 0.00 | 0.00 | -19 |
| MLTX-02-005-EN | Shop DWG Approval for Water Supply Layout | 21 | 100% | 100% | 23-May-26 | 18-Jun-26 | 18-Mar-26 A | 03-Jun-26 A | 0.00 | 0.00 | 0.00 | 13 |
| MLTX-02-005-EN | Shop DWG Approval for Water Supply Details | 21 | 100% | 100% | 23-May-26 | 18-Jun-26 | 18-Mar-26 A | 03-Jun-26 A | 0.00 | 0.00 | 0.00 | 13 |
| MLTX-02-005-EN | Shop DWG Approval for Drainage Layout | 21 | 100% | 100% | 23-May-26 | 18-Jun-26 | 18-Mar-26 A | 03-Jun-26 A | 0.00 | 0.00 | 0.00 | 13 |
| MLTX-02-005-EN | Shop DWG Approval for Drainage Details | 21 | 100% | 100% | 23-May-26 | 18-Jun-26 | 18-Mar-26 A | 03-Jun-26 A | 0.00 | 0.00 | 0.00 | 13 |
| MLTX-02-005-EN | Shop DWG Approval for Duct Routing Layout | 21 | 100% | 100% | 23-May-26 | 18-Jun-26 | 11-Jul-26 A | 11-Jul-26 A | 0.00 | 0.00 | 0.00 | -19 |
| MLTX-02-005-EN | Shop DWG Approval for Diffusers Layout | 21 | 100% | 100% | 23-May-26 | 18-Jun-26 | 11-Jul-26 A | 11-Jul-26 A | 0.00 | 0.00 | 0.00 | -19 |
| **ELECTRICAL WORKS** | | 40 | 0% | 0% | 16-May-26 | 22-Jun-26 | 18-Mar-26 A | 28-Jul-26 A | 0.00 | 0.00 | 0.00 | -31 |
| MLTX-02-005-EN | Shop DWG Approval for Lighting Layout | 21 | 100% | 100% | 23-May-26 | 18-Jun-26 | 24-Mar-26 A | 04-Apr-26 A | 0.00 | 0.00 | 0.00 | 62 |
| MLTX-02-005-EN | Shop DWG Approval for Power Layout | 21 | 100% | 100% | 23-May-26 | 18-Jun-26 | 24-Mar-26 A | 04-Apr-26 A | 0.00 | 0.00 | 0.00 | 62 |
| MLTX-02-005-EN | Shop DWG Approval for Power Single Line Diagram | 21 | 100% | 100% | 23-May-26 | 18-Jun-26 | 18-Mar-26 A | 07-May-26 A | 0.00 | 0.00 | 0.00 | 33 |
| MLTX-02-005-EN | Shop DWG Approval for Panel Board Schedules | 21 | 100% | 100% | 16-May-26 | 11-Jun-26 | 18-Mar-26 A | 07-May-26 A | 0.00 | 0.00 | 0.00 | 27 |
| MLTX-02-005-EN | Shop DWG Approval for Lighting Installation Details | 21 | 100% | 100% | 23-May-26 | 18-Jun-26 | 24-Mar-26 A | 04-Apr-26 A | 0.00 | 0.00 | 0.00 | 62 |
| MLTX-02-005-EN | Shop DWG Approval for Power Installation Details | 21 | 100% | 100% | 16-May-26 | 11-Jun-26 | 24-Mar-26 A | 04-Apr-26 A | 0.00 | 0.00 | 0.00 | 56 |
| MLTX-02-005-EN | Shop DWG Approval for Cable Tray Installation Details | 21 | 100% | 100% | 16-May-26 | 11-Jun-26 | 18-Mar-26 A | 07-May-26 A | 0.00 | 0.00 | 0.00 | 27 |
| MLTX-02-005-EN | Shop DWG Approval for Manhole & Ductbank Details | 21 | 100% | 100% | 16-May-26 | 11-Jun-26 | 18-Mar-26 A | 07-May-26 A | 0.00 | 0.00 | 0.00 | 27 |
| MLTX-02-005-EN | Shop DWG Approval for Grounding Details | 21 | 100% | 100% | 16-May-26 | 11-Jun-26 | 24-Mar-26 A | 04-Apr-26 A | 0.00 | 0.00 | 0.00 | 56 |
| MLTX-02-005-EN | Shop DWG Approval for Lightning Protection Details | 21 | 100% | 100% | 16-May-26 | 11-Jun-26 | 24-Mar-26 A | 04-Apr-26 A | 0.00 | 0.00 | 0.00 | 56 |
| MLTX-02-005-EN | Shop DWG Approval for Fire Alarm Installation Details | 21 | 100% | 100% | 16-May-26 | 11-Jun-26 | 24-Mar-26 A | 04-Apr-26 A | 0.00 | 0.00 | 0.00 | 56 |
| MLTX-02-005-EN | Shop DWG Approval for CCTV Details | 30 | 100% | 100% | 16-May-26 | 22-Jun-26 | 28-Jul-26 A | 28-Jul-26 A | 0.00 | 0.00 | 0.00 | -31 |
| MLTX-02-005-EN | Shop DWG Approval for Grounding Layout | 21 | 100% | 100% | 16-May-26 | 11-Jun-26 | 24-Mar-26 A | 04-Apr-26 A | 0.00 | 0.00 | 0.00 | 56 |
| MLTX-02-005-EN | Shop DWG Approval for Lightning Protection System Layout | 21 | 100% | 100% | 16-May-26 | 11-Jun-26 | 24-Mar-26 A | 04-Apr-26 A | 0.00 | 0.00 | 0.00 | 56 |
| MLTX-02-005-EN | Shop DWG Approval for Fire Alarm Layout | 21 | 100% | 100% | 16-May-26 | 11-Jun-26 | 24-Mar-26 A | 04-Apr-26 A | 0.00 | 0.00 | 0.00 | 56 |
| MLTX-02-005-EN | Shop DWG Approval for Fire Alarm Riser Diagram | 21 | 100% | 100% | 16-May-26 | 11-Jun-26 | 24-Mar-26 A | 04-Apr-26 A | 0.00 | 0.00 | 0.00 | 56 |
| MLTX-02-005-EN | Shop DWG Approval for CCTV Layout | 30 | 100% | 100% | 16-May-26 | 22-Jun-26 | 24-Mar-26 A | 04-Apr-26 A | 0.00 | 0.00 | 0.00 | 65 |
| MLTX-02-005-EN | Shop DWG Approval for CCTV Riser Diagram | 30 | 100% | 100% | 16-May-26 | 22-Jun-26 | 24-Mar-26 A | 04-Apr-26 A | 0.00 | 0.00 | 0.00 | 65 |
| MLTX-02-005-EN | Shop DWG Approval for Telephone & Data Layout | 21 | 100% | 100% | 23-May-26 | 18-Jun-26 | 24-Mar-26 A | 04-Apr-26 A | 0.00 | 0.00 | 0.00 | 62 |
| MLTX-02-005-EN | Shop DWG Approval for Telephone & Data Riser Diagram | 21 | 100% | 100% | 23-May-26 | 18-Jun-26 | 24-Mar-26 A | 04-Apr-26 A | 0.00 | 0.00 | 0.00 | 62 |
| **SHOP DRAWINGS APPROVAL FOR PLAYGROUND WORKS** | | 164 | 0% | 0% | 30-Mar-26 | 24-May-26 | 14-Mar-26 A | 28-Jan-27 | 0.00 | 0.00 | 0.00 | -210 |
| **ARCHITECTURE WORKS** | | 30 | 0% | 0% | 30-Mar-26 | 03-May-26 | 14-Mar-26 A | 19-May-26 A | 0.00 | 0.00 | 0.00 | -14 |
| MLTX-02-005-EN | Shop DWG Approval for Playground Plan/Layout | 15 | 100% | 100% | 30-Mar-26 | 15-Apr-26 | 14-Mar-26 A | 19-May-26 A | 0.00 | 0.00 | 0.00 | -29 |
| MLTX-02-005-EN | Shop DWG Approval for Furniture & Marking | 30 | 100% | 100% | 30-Mar-26 | 03-May-26 | 14-Mar-26 A | 19-May-26 A | 0.00 | 0.00 | 0.00 | -14 |
| MLTX-02-005-EN | Shop DWG Approval for Sections | 15 | 100% | 100% | 30-Mar-26 | 15-Apr-26 | 14-Mar-26 A | 19-May-26 A | 0.00 | 0.00 | 0.00 | -29 |
| MLTX-02-005-EN | Shop DWG Approval for Interlock Pattern Plan | 21 | 100% | 100% | 06-Apr-26 | 29-Apr-26 | 14-Mar-26 A | 19-May-26 A | 0.00 | 0.00 | 0.00 | -17 |

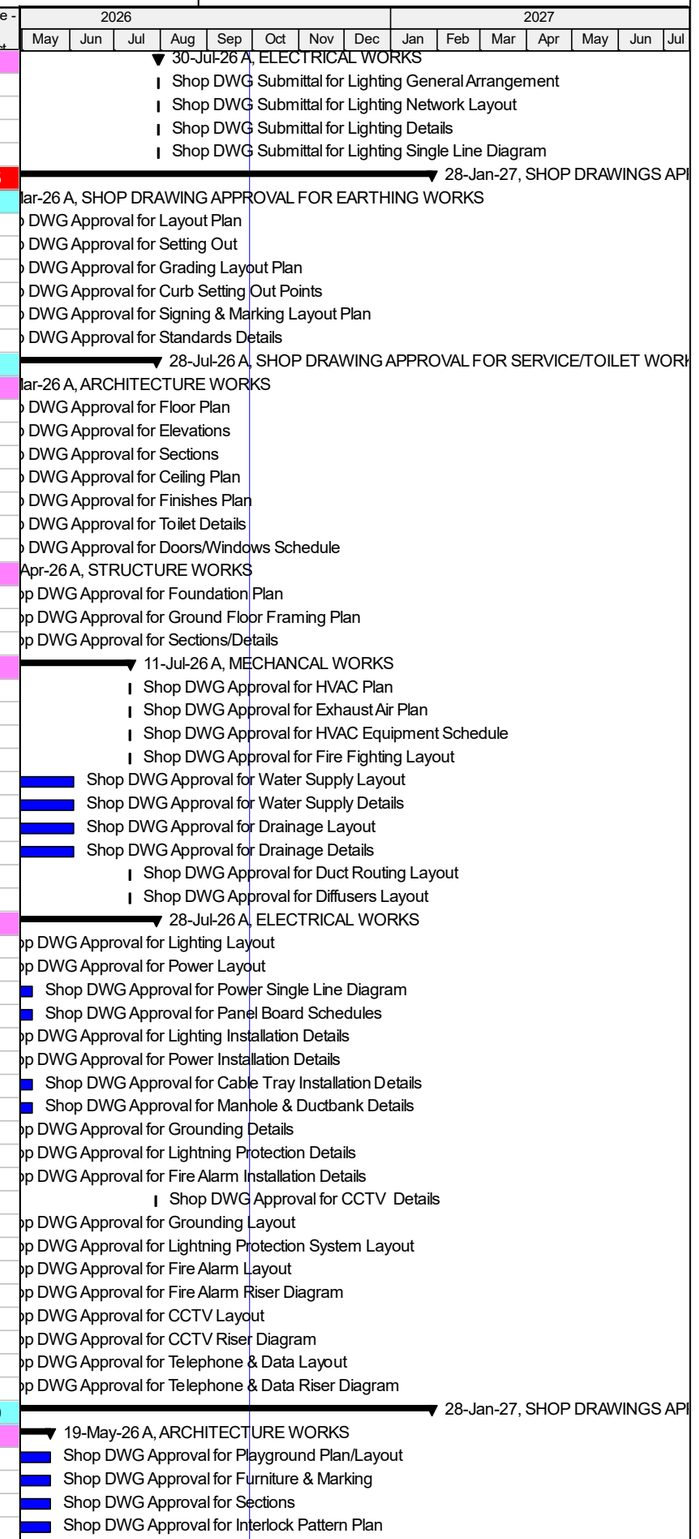


Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary




TASK filter: All Activities

© Oracle Corporation

# MLTX-02-005 - Playground Initiative for Eastern Region (Arar-Hasa osis -Dammam)

**Updateded schedule**
**D.D 28-09-2026**

| Activity ID | Activity Name | Original Duration | Schedule % Complete | Performance % Complete | BL Project Start | BL Project Finish | Start | Finish | Planned Value Cost | Earned Value Cost | Budgeted Total Cost | Variance - BL Project |
|---|---|---|---|---|---|---|---|---|---|---|---|---|
| MLTX-02-005-EN | Shop DWG Approval for Doors/Windows Schedule | 21 | 100% | 100% | 06-Apr-26 | 29-Apr-26 | 14-Mar-26 A | 19-May-26 A | 0.00 | 0.00 | 0.00 | -17 |
| MLTX-02-005-EN | Shop DWG Approval for Dome Internal Layout | 21 | 100% | 100% | 06-Apr-26 | 29-Apr-26 | 14-Mar-26 A | 19-May-26 A | 0.00 | 0.00 | 0.00 | -17 |
| **STRUCTURE WORKS** | | 21 | 0% | 0% | 30-Apr-26 | 24-May-26 | 16-Jul-26 A | 16-Jul-26 A | 0.00 | 0.00 | 0.00 | -43 |
| MLTX-02-005-EN | Shop DWG Approval for Air Dome System | 21 | 100% | 100% | 30-Apr-26 | 24-May-26 | 16-Jul-26 A | 16-Jul-26 A | 0.00 | 0.00 | 0.00 | -43 |
| MLTX-02-005-EN | Shop DWG Approval for Foundation of Air Dome | 21 | 100% | 100% | 30-Apr-26 | 24-May-26 | 16-Jul-26 A | 16-Jul-26 A | 0.00 | 0.00 | 0.00 | -43 |
| MLTX-02-005-EN | Shop DWG Approval for Foundation of Air Dome | 21 | 100% | 100% | 30-Apr-26 | 24-May-26 | 16-Jul-26 A | 16-Jul-26 A | 0.00 | 0.00 | 0.00 | -43 |
| MLTX-02-005-EN | Shop DWG Approval for Anchor Bolt Layout of Air Dome | 21 | 100% | 100% | 30-Apr-26 | 24-May-26 | 16-Jul-26 A | 16-Jul-26 A | 0.00 | 0.00 | 0.00 | -43 |
| **AIR DOME SYSTEM** | | 84 | 0% | 0% | 30-Apr-26 | 24-May-26 | 29-Sep-26 | 04-Jan-27 | 0.00 | 0.00 | 0.00 | -189 |
| MLTX-02-005-EN | Shop DWG Approval for Air Dome Structural Layout | 21 | 100% | 0% | 30-Apr-26 | 24-May-26 | 29-Sep-26 | 22-Oct-26 | 0.00 | 0.00 | 0.00 | -126 |
| MLTX-02-005-EN | Shop DWG Approval for Membrane Panel Layout | 21 | 100% | 0% | 30-Apr-26 | 24-May-26 | 24-Oct-26 | 16-Nov-26 | 0.00 | 0.00 | 0.00 | -147 |
| MLTX-02-005-EN | Shop DWG Approval for Cable Tension Layout | 21 | 100% | 0% | 30-Apr-26 | 24-May-26 | 24-Oct-26 | 16-Nov-26 | 0.00 | 0.00 | 0.00 | -147 |
| MLTX-02-005-EN | Shop DWG Approval for Airlock Door Details | 21 | 100% | 0% | 30-Apr-26 | 24-May-26 | 17-Nov-26 | 10-Dec-26 | 0.00 | 0.00 | 0.00 | -168 |
| MLTX-02-005-EN | Shop DWG Approval for Emergency Exit Details | 21 | 100% | 0% | 30-Apr-26 | 24-May-26 | 12-Dec-26 | 04-Jan-27 | 0.00 | 0.00 | 0.00 | -189 |
| **SPORTS EQUIPMENT** | | 68 | 0% | 0% | 30-Apr-26 | 24-May-26 | 20-Jul-26 A | 22-Oct-26 | 0.00 | 0.00 | 0.00 | -126 |
| MLTX-02-005-EN | Shop DWG Approval for Football Turf Installation | 21 | 100% | 0% | 30-Apr-26 | 24-May-26 | 29-Sep-26 | 22-Oct-26 | 0.00 | 0.00 | 0.00 | -126 |
| MLTX-02-005-EN | Shop DWG Approval for Basketball Court Marking | 21 | 100% | 100% | 30-Apr-26 | 24-May-26 | 25-Aug-26 A | 25-Aug-26 A | 0.00 | 0.00 | 0.00 | -77 |
| MLTX-02-005-EN | Shop DWG Approval for Padel Court Structure | 21 | 100% | 100% | 30-Apr-26 | 24-May-26 | 20-Jul-26 A | 20-Jul-26 A | 0.00 | 0.00 | 0.00 | -46 |
| **MECHANCAL WORKS** | | 84 | 0% | 0% | 30-Apr-26 | 24-May-26 | 24-Oct-26 | 28-Jan-27 | 0.00 | 0.00 | 0.00 | -210 |
| MLTX-02-005-EN | Shop DWG Approval for HVAC Plan | 21 | 100% | 0% | 30-Apr-26 | 24-May-26 | 24-Oct-26 | 16-Nov-26 | 0.00 | 0.00 | 0.00 | -147 |
| MLTX-02-005-EN | Shop DWG Approval for Exhaust Air Plan | 21 | 100% | 0% | 30-Apr-26 | 24-May-26 | 05-Jan-27 | 28-Jan-27 | 0.00 | 0.00 | 0.00 | -210 |
| **ELECTRICAL WORKS** | | 74 | 0% | 0% | 30-Apr-26 | 24-May-26 | 19-Mar-26 A | 16-Nov-26 | 0.00 | 0.00 | 0.00 | -147 |
| MLTX-02-005-EN | Shop DWG Approval for Lighting Layout | 21 | 100% | 100% | 30-Apr-26 | 24-May-26 | 19-Mar-26 A | 18-May-26 A | 0.00 | 0.00 | 0.00 | 5 |
| MLTX-02-005-EN | Shop DWG Approval for Power Layout | 21 | 100% | 0% | 30-Apr-26 | 24-May-26 | 24-Oct-26 | 16-Nov-26 | 0.00 | 0.00 | 0.00 | -147 |
| MLTX-02-005-EN | Shop DWG Approval for Power Single Line Diagram | 21 | 100% | 0% | 30-Apr-26 | 24-May-26 | 24-Oct-26 | 16-Nov-26 | 0.00 | 0.00 | 0.00 | -147 |
| MLTX-02-005-EN | Shop DWG Approval for Panel Board Schedules | 21 | 100% | 0% | 30-Apr-26 | 24-May-26 | 24-Oct-26 | 16-Nov-26 | 0.00 | 0.00 | 0.00 | -147 |
| MLTX-02-005-EN | Shop DWG Approval for Power Installation Details | 21 | 100% | 0% | 30-Apr-26 | 24-May-26 | 24-Oct-26 | 16-Nov-26 | 0.00 | 0.00 | 0.00 | -147 |
| MLTX-02-005-EN | Shop DWG Approval for CCTV Details | 21 | 100% | 100% | 30-Apr-26 | 24-May-26 | 25-Aug-26 A | 25-Aug-26 A | 0.00 | 0.00 | 0.00 | -77 |
| MLTX-02-005-EN | Shop DWG Approval for CCTV Layout | 21 | 100% | 100% | 30-Apr-26 | 24-May-26 | 25-Aug-26 A | 25-Aug-26 A | 0.00 | 0.00 | 0.00 | -77 |
| MLTX-02-005-EN | Shop DWG Approval for CCTV Riser Diagram | 21 | 100% | 100% | 30-Apr-26 | 24-May-26 | 25-Aug-26 A | 25-Aug-26 A | 0.00 | 0.00 | 0.00 | -77 |
| **SHOP DRAWINGS APPROVAL FOR LANDSCAPE WORKS** | | 72 | 0% | 0% | 30-Mar-26 | 20-May-26 | 14-Mar-26 A | 30-Jul-26 A | 0.00 | 0.00 | 0.00 | -58 |
| **ARCHITECTURE WORKS** | | 30 | 0% | 0% | 30-Mar-26 | 03-May-26 | 14-Mar-26 A | 06-May-26 A | 0.00 | 0.00 | 0.00 | -3 |
| MLTX-02-005-EN | Shop DWG Approval for Landscape Layout | 21 | 100% | 100% | 06-Apr-26 | 29-Apr-26 | 14-Mar-26 A | 14-Apr-26 A | 0.00 | 0.00 | 0.00 | 13 |
| MLTX-02-005-EN | Shop DWG Approval for Hardscape Plan | 21 | 100% | 100% | 06-Apr-26 | 29-Apr-26 | 14-Mar-26 A | 14-Apr-26 A | 0.00 | 0.00 | 0.00 | 13 |
| MLTX-02-005-EN | Shop DWG Approval for Planting Plan | 15 | 100% | 100% | 16-Apr-26 | 03-May-26 | 19-Mar-26 A | 06-May-26 A | 0.00 | 0.00 | 0.00 | -3 |
| MLTX-02-005-EN | Shop DWG Approval for Landscape Details | 21 | 100% | 100% | 30-Mar-26 | 22-Apr-26 | 14-Mar-26 A | 14-Apr-26 A | 0.00 | 0.00 | 0.00 | 7 |
| **MECHANCAL WORKS** | | 21 | 0% | 0% | 06-Apr-26 | 29-Apr-26 | 30-Jul-26 A | 30-Jul-26 A | 0.00 | 0.00 | 0.00 | -76 |
| MLTX-02-005-EN | Shop DWG Approval for Irrigation Details | 21 | 100% | 100% | 06-Apr-26 | 29-Apr-26 | 30-Jul-26 A | 30-Jul-26 A | 0.00 | 0.00 | 0.00 | -76 |
| MLTX-02-005-EN | Shop DWG Approval for Irrigation Layout | 21 | 100% | 100% | 06-Apr-26 | 29-Apr-26 | 30-Jul-26 A | 30-Jul-26 A | 0.00 | 0.00 | 0.00 | -76 |
| **ELECTRICAL WORKS** | | 30 | 0% | 0% | 16-Apr-26 | 20-May-26 | 30-Jul-26 A | 30-Jul-26 A | 0.00 | 0.00 | 0.00 | -58 |
| MLTX-02-005-EN | Shop DWG Approval for Lighting General Arrangement | 30 | 100% | 100% | 16-Apr-26 | 20-May-26 | 30-Jul-26 A | 30-Jul-26 A | 0.00 | 0.00 | 0.00 | -58 |
| MLTX-02-005-EN | Shop DWG Approval for Lighting Network Layout | 30 | 100% | 100% | 16-Apr-26 | 20-May-26 | 30-Jul-26 A | 30-Jul-26 A | 0.00 | 0.00 | 0.00 | -58 |
| MLTX-02-005-EN | Shop DWG Approval for Lighting Details | 30 | 100% | 100% | 16-Apr-26 | 20-May-26 | 30-Jul-26 A | 30-Jul-26 A | 0.00 | 0.00 | 0.00 | -58 |
| MLTX-02-005-EN | Shop DWG Approval for Lighting Single Line Diagram | 30 | 100% | 100% | 16-Apr-26 | 20-May-26 | 30-Jul-26 A | 30-Jul-26 A | 0.00 | 0.00 | 0.00 | -58 |
| **METHOD STATEMENTS** | | 87 | 0% | 0% | 09-Mar-26 | 28-Jun-26 | 08-Mar-26 A | 12-Sep-26 A | 0.00 | 0.00 | 0.00 | -65 |
| **METHOD STATEMENT SUBMITTAL** | | 60 | 0% | 0% | 09-Mar-26 | 20-May-26 | 08-Mar-26 A | 04-Jun-26 A | 0.00 | 0.00 | 0.00 | -10 |
| **CIVIL WORKS** | | 21 | 0% | 0% | 09-Mar-26 | 05-Apr-26 | 09-Mar-26 A | 14-Mar-26 A | 0.00 | 0.00 | 0.00 | 16 |
| MLTX-02-005-EN-1 | Preparation & Submission of Method Statement for | 15 | 100% | 100% | 09-Mar-26 | 29-Mar-26 | 09-Mar-26 A | 14-Mar-26 A | 0.00 | 0.00 | 0.00 | 10 |
| MLTX-02-005-EN-1 | Preparation & Submission of Method Statement for Concrete | 21 | 100% | 100% | 09-Mar-26 | 05-Apr-26 | 09-Mar-26 A | 14-Mar-26 A | 0.00 | 0.00 | 0.00 | 16 |
| MLTX-02-005-EN-1 | Preparation & Submission of Method Statement for | 21 | 100% | 100% | 09-Mar-26 | 05-Apr-26 | 09-Mar-26 A | 14-Mar-26 A | 0.00 | 0.00 | 0.00 | 16 |
| **ARCHITECTURE WORKS** | | 30 | 0% | 0% | 09-Mar-26 | 15-Apr-26 | 08-Mar-26 A | 02-Jun-26 A | 0.00 | 0.00 | 0.00 | -38 |
| MLTX-02-005-EN-1 | Preparation & Submission of Method Statement for Plastering | 15 | 100% | 100% | 09-Mar-26 | 29-Mar-26 | 09-Mar-26 A | 14-Mar-26 A | 0.00 | 0.00 | 0.00 | 10 |
| MLTX-02-005-EN-1 | Preparation & Submission of Method Statement for | 21 | 100% | 100% | 09-Mar-26 | 05-Apr-26 | 08-Mar-26 A | 17-May-26 A | 0.00 | 0.00 | 0.00 | -36 |
| MLTX-02-005-EN-1 | Preparation & Submission of Method Statement for Tilling | 21 | 100% | 100% | 09-Mar-26 | 05-Apr-26 | 08-Mar-26 A | 25-May-26 A | 0.00 | 0.00 | 0.00 | -43 |
| MLTX-02-005-EN-1 | Preparation & Submission of Method Statement for | 21 | 100% | 100% | 09-Mar-26 | 05-Apr-26 | 08-Mar-26 A | 02-Jun-26 A | 0.00 | 0.00 | 0.00 | -47 |
| MLTX-02-005-EN-1 | Preparation & Submission of Method Statement for | 21 | 100% | 100% | 09-Mar-26 | 05-Apr-26 | 08-Mar-26 A | 02-Jun-26 A | 0.00 | 0.00 | 0.00 | -47 |
| MLTX-02-005-EN-1 | Preparation & Submission of Method Statement for | 21 | 100% | 100% | 09-Mar-26 | 05-Apr-26 | 08-Mar-26 A | 25-May-26 A | 0.00 | 0.00 | 0.00 | -43 |
| MLTX-02-005-EN-1 | Preparation & Submission of Method Statement for Parking | 21 | 100% | 100% | 09-Mar-26 | 05-Apr-26 | 08-Mar-26 A | 25-May-26 A | 0.00 | 0.00 | 0.00 | -43 |
| MLTX-02-005-EN-1 | Preparation & Submission of Method Statement for Soft | 21 | 100% | 100% | 09-Mar-26 | 05-Apr-26 | 08-Mar-26 A | 02-Jun-26 A | 0.00 | 0.00 | 0.00 | -47 |
| MLTX-02-005-EN-1 | Preparation & Submission of Method Statement for Fence | 30 | 100% | 100% | 09-Mar-26 | 15-Apr-26 | 08-Mar-26 A | 02-Jun-26 A | 0.00 | 0.00 | 0.00 | -38 |
| MLTX-02-005-EN-1 | Preparation & Submission of Method Statement for Air Dome | 30 | 100% | 100% | 09-Mar-26 | 15-Apr-26 | 08-Mar-26 A | 02-Jun-26 A | 0.00 | 0.00 | 0.00 | -38 |
| MLTX-02-005-EN-1 | Preparation & Submission of Method Statement for Metal | 21 | 100% | 100% | 09-Mar-26 | 05-Apr-26 | 08-Mar-26 A | 02-Jun-26 A | 0.00 | 0.00 | 0.00 | -47 |
| MLTX-02-005-EN-1 | Preparation & Submission of Method Statement for Partitions | 21 | 100% | 100% | 09-Mar-26 | 05-Apr-26 | 08-Mar-26 A | 02-Jun-26 A | 0.00 | 0.00 | 0.00 | -47 |
| MLTX-02-005-EN-1 | Preparation & Submission of Method Statement for Gypsum | 21 | 100% | 100% | 09-Mar-26 | 05-Apr-26 | 08-Mar-26 A | 02-Jun-26 A | 0.00 | 0.00 | 0.00 | -47 |
| **MECHANICAL WORKS** | | 27 | 0% | 0% | 30-Mar-26 | 29-Apr-26 | 14-Mar-26 A | 04-Jun-26 A | 0.00 | 0.00 | 0.00 | -28 |

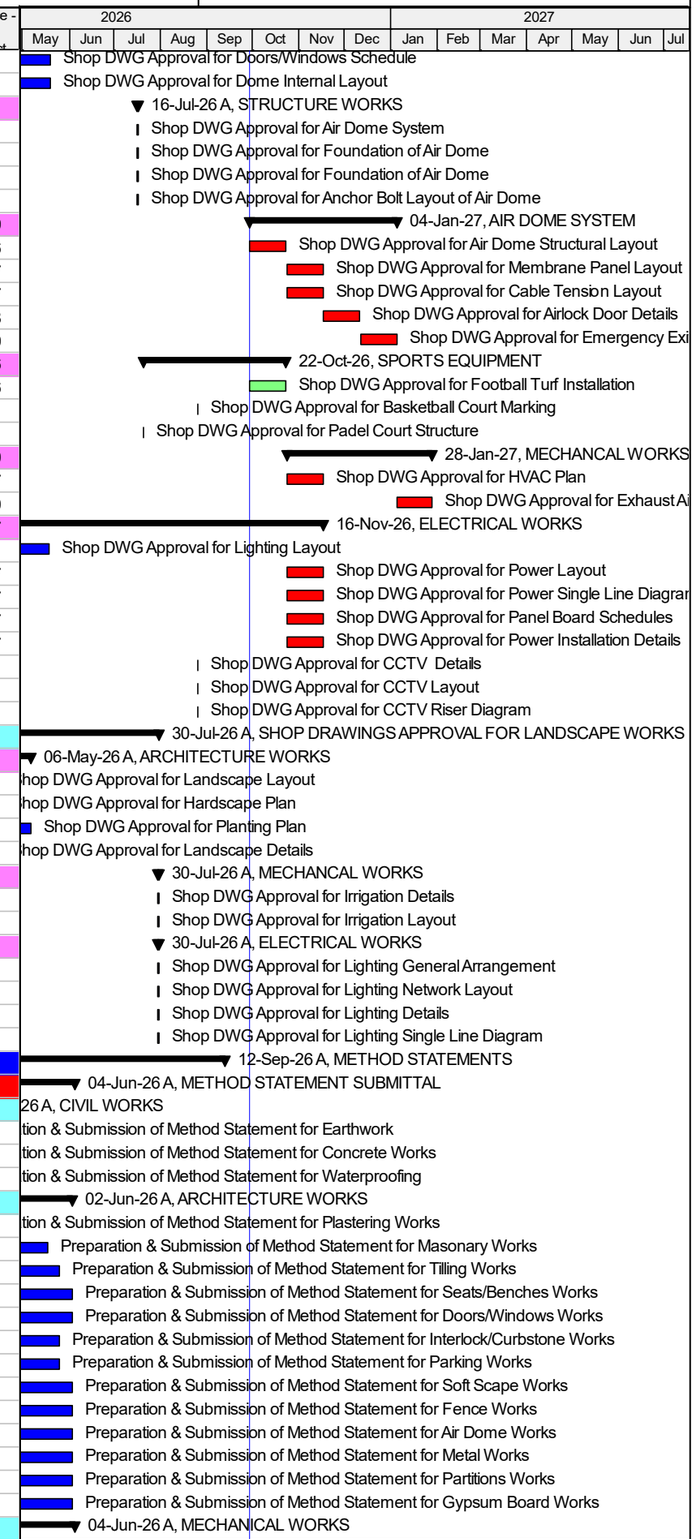





© Oracle Corporation

# MLTX-02-005 - Playground Initiative for Eastern Region (Arar-Hasa osis -Dammam)

**Updateded schedule**
**D.D 28-09-2026**

| Activity ID | Activity Name | Original Duration | Schedule % Complete | Performance % Complete | BL Project Start | BL Project Finish | Start | Finish | Planned Value Cost | Earned Value Cost | Budgeted Total Cost | Variance - BL Project |
|---|---|---|---|---|---|---|---|---|---|---|---|---|
| MLTX-02-005-EN-1 | Preparation & Submission of Method Statement for | 21 | 100% | 100% | 30-Mar-26 | 22-Apr-26 | 14-Mar-26 A | 04-May-26 A | 0.00 | 0.00 | 0.00 | -10 |
| MLTX-02-005-EN-1 | Preparation & Submission of Method Statement for Water | 21 | 100% | 100% | 06-Apr-26 | 29-Apr-26 | 14-Mar-26 A | 04-May-26 A | 0.00 | 0.00 | 0.00 | -4 |
| MLTX-02-005-EN-1 | Preparation & Submission of Method Statement for Fire | 21 | 100% | 100% | 06-Apr-26 | 29-Apr-26 | 14-Mar-26 A | 04-Jun-26 A | 0.00 | 0.00 | 0.00 | -28 |
| MLTX-02-005-EN-1 | Preparation & Submission of Method Statement for Irrigation | 15 | 100% | 100% | 30-Mar-26 | 15-Apr-26 | 14-Mar-26 A | 04-Jun-26 A | 0.00 | 0.00 | 0.00 | -40 |
| MLTX-02-005-EN-1 | Preparation & Submission of Method Statement for HVAC | 21 | 100% | 100% | 06-Apr-26 | 29-Apr-26 | 14-Mar-26 A | 04-Jun-26 A | 0.00 | 0.00 | 0.00 | -28 |
| **ELECTRICAL WORKS** | | 39 | 0% | 0% | 06-Apr-26 | 20-May-26 | 14-Mar-26 A | 11-May-26 A | 0.00 | 0.00 | 0.00 | 8 |
| MLTX-02-005-EN-1 | Preparation & Submission of Method Statement for Electrical | 21 | 100% | 100% | 06-Apr-26 | 29-Apr-26 | 14-Mar-26 A | 11-May-26 A | 0.00 | 0.00 | 0.00 | -10 |
| MLTX-02-005-EN-1 | Preparation & Submission of Method Statement for Lighting | 21 | 100% | 100% | 06-Apr-26 | 29-Apr-26 | 14-Mar-26 A | 11-May-26 A | 0.00 | 0.00 | 0.00 | -10 |
| MLTX-02-005-EN-1 | Preparation & Submission of Method Statement for | 30 | 100% | 100% | 16-Apr-26 | 20-May-26 | 14-Mar-26 A | 11-May-26 A | 0.00 | 0.00 | 0.00 | 8 |
| MLTX-02-005-EN-1 | Preparation & Submission of Method Statement for CCTV | 30 | 100% | 100% | 16-Apr-26 | 20-May-26 | 14-Mar-26 A | 11-May-26 A | 0.00 | 0.00 | 0.00 | 8 |
| MLTX-02-005-EN-1 | Preparation & Submission of Method Statement for Lighting | 21 | 100% | 100% | 06-Apr-26 | 29-Apr-26 | 14-Mar-26 A | 11-May-26 A | 0.00 | 0.00 | 0.00 | -10 |
| MLTX-02-005-EN-1 | Preparation & Submission of Method Statement for | 21 | 100% | 100% | 06-Apr-26 | 29-Apr-26 | 14-Mar-26 A | 11-May-26 A | 0.00 | 0.00 | 0.00 | -10 |
| MLTX-02-005-EN-1 | Preparation & Submission of Method Statement for Panel | 21 | 100% | 100% | 06-Apr-26 | 29-Apr-26 | 14-Mar-26 A | 11-May-26 A | 0.00 | 0.00 | 0.00 | -10 |
| **METHOD STATEMENT APPROVAL** | | 72 | 0% | 0% | 30-Mar-26 | 28-Jun-26 | 14-Mar-26 A | 12-Sep-26 A | 0.00 | 0.00 | 0.00 | -65 |
| **CIVIL WORKS** | | 36 | 0% | 0% | 30-Mar-26 | 10-May-26 | 15-Mar-26 A | 29-Mar-26 A | 0.00 | 0.00 | 0.00 | 36 |
| MLTX-02-005-EN-1 | Approval of Method Statement for Earthwork | 15 | 100% | 100% | 30-Mar-26 | 15-Apr-26 | 15-Mar-26 A | 29-Mar-26 A | 0.00 | 0.00 | 0.00 | 15 |
| MLTX-02-005-EN-1 | Approval of Method Statement for Concrete Works | 30 | 100% | 100% | 06-Apr-26 | 10-May-26 | 15-Mar-26 A | 29-Mar-26 A | 0.00 | 0.00 | 0.00 | 36 |
| MLTX-02-005-EN-1 | Approval of Method Statement for Waterproofing | 21 | 100% | 100% | 06-Apr-26 | 29-Apr-26 | 15-Mar-26 A | 29-Mar-26 A | 0.00 | 0.00 | 0.00 | 27 |
| **ARCHITECTURE WORKS** | | 69 | 0% | 0% | 30-Mar-26 | 20-May-26 | 14-Mar-26 A | 12-Sep-26 A | 0.00 | 0.00 | 0.00 | -95 |
| MLTX-02-005-EN-1 | Approval of Method Statement for Plastering Works | 30 | 100% | 100% | 30-Mar-26 | 03-May-26 | 15-Mar-26 A | 29-Mar-26 A | 0.00 | 0.00 | 0.00 | 30 |
| MLTX-02-005-EN-1 | Approval of Method Statement for Masonary Works | 21 | 100% | 100% | 06-Apr-26 | 29-Apr-26 | 14-Mar-26 A | 21-May-26 A | 0.00 | 0.00 | 0.00 | -19 |
| MLTX-02-005-EN-1 | Approval of Method Statement for Tilling Works | 21 | 100% | 100% | 06-Apr-26 | 29-Apr-26 | 14-Mar-26 A | 21-May-26 A | 0.00 | 0.00 | 0.00 | -19 |
| MLTX-02-005-EN-1 | Approval of Method Statement for Seats/Benches Works | 21 | 100% | 100% | 06-Apr-26 | 29-Apr-26 | 12-Sep-26 A | 12-Sep-26 A | 0.00 | 0.00 | 0.00 | -113 |
| MLTX-02-005-EN-1 | Approval of Method Statement for Doors/Windows Works | 21 | 100% | 100% | 06-Apr-26 | 29-Apr-26 | 12-Sep-26 A | 12-Sep-26 A | 0.00 | 0.00 | 0.00 | -113 |
| MLTX-02-005-EN-1 | Approval of Method Statement for Interlock/Curbstone Works | 21 | 100% | 100% | 06-Apr-26 | 29-Apr-26 | 10-Aug-26 A | 10-Aug-26 A | 0.00 | 0.00 | 0.00 | -85 |
| MLTX-02-005-EN-1 | Approval of Method Statement for Parking Works | 21 | 100% | 100% | 06-Apr-26 | 29-Apr-26 | 15-May-26 A | 15-May-26 A | 0.00 | 0.00 | 0.00 | -13 |
| MLTX-02-005-EN-1 | Approval of Method Statement for Soft Scape Works | 21 | 100% | 100% | 06-Apr-26 | 29-Apr-26 | 12-Sep-26 A | 12-Sep-26 A | 0.00 | 0.00 | 0.00 | -113 |
| MLTX-02-005-EN-1 | Approval of Method Statement for Fence Works | 30 | 100% | 100% | 16-Apr-26 | 20-May-26 | 16-Jul-26 A | 16-Jul-26 A | 0.00 | 0.00 | 0.00 | -46 |
| MLTX-02-005-EN-1 | Approval of Method Statement for Air Dome Works | 30 | 100% | 100% | 16-Apr-26 | 20-May-26 | 12-Jul-26 A | 12-Jul-26 A | 0.00 | 0.00 | 0.00 | -42 |
| MLTX-02-005-EN-1 | Approval of Method Statement for Partitions Works | 21 | 100% | 100% | 06-Apr-26 | 29-Apr-26 | 12-Sep-26 A | 12-Sep-26 A | 0.00 | 0.00 | 0.00 | -113 |
| MLTX-02-005-EN-1 | Approval of Method Statement for Gypsum Board Works | 21 | 100% | 100% | 06-Apr-26 | 29-Apr-26 | 20-Aug-26 A | 20-Aug-26 A | 0.00 | 0.00 | 0.00 | -94 |
| **MECHANICAL WORKS** | | 54 | 0% | 0% | 16-Apr-26 | 24-May-26 | 24-Jun-26 A | 26-Aug-26 A | 0.00 | 0.00 | 0.00 | -78 |
| MLTX-02-005-EN-1 | Approval of Method Statement for Sewage/Drainage System | 21 | 100% | 100% | 23-Apr-26 | 17-May-26 | 24-Jun-26 A | 24-Jun-26 A | 0.00 | 0.00 | 0.00 | -30 |
| MLTX-02-005-EN-1 | Approval of Method Statement for Water Supply System | 21 | 100% | 100% | 30-Apr-26 | 24-May-26 | 12-Jul-26 A | 18-Jul-26 A | 0.00 | 0.00 | 0.00 | -44 |
| MLTX-02-005-EN-1 | Approval of Method Statement for Fire Fighting System | 21 | 100% | 100% | 30-Apr-26 | 24-May-26 | 26-Aug-26 A | 26-Aug-26 A | 0.00 | 0.00 | 0.00 | -78 |
| MLTX-02-005-EN-1 | Approval of Method Statement for Irrigation System | 15 | 100% | 100% | 16-Apr-26 | 03-May-26 | 25-Aug-26 A | 25-Aug-26 A | 0.00 | 0.00 | 0.00 | -95 |
| MLTX-02-005-EN-1 | Approval of Method Statement for HVAC System | 21 | 100% | 100% | 30-Apr-26 | 24-May-26 | 18-Aug-26 A | 18-Aug-26 A | 0.00 | 0.00 | 0.00 | -71 |
| **ELECTRICAL WORKS** | | 72 | 0% | 0% | 30-Apr-26 | 28-Jun-26 | 14-Jul-26 A | 26-Aug-26 A | 0.00 | 0.00 | 0.00 | -51 |
| MLTX-02-005-EN-1 | Approval of Method Statement for Electrical Conduits/Pulling | 21 | 100% | 100% | 30-Apr-26 | 24-May-26 | 14-Jul-26 A | 14-Jul-26 A | 0.00 | 0.00 | 0.00 | -41 |
| MLTX-02-005-EN-1 | Approval of Method Statement for Lighting Poles Installation | 21 | 100% | 100% | 30-Apr-26 | 24-May-26 | 26-Aug-26 A | 26-Aug-26 A | 0.00 | 0.00 | 0.00 | -78 |
| MLTX-02-005-EN-1 | Approval of Method Statement for Telecommunication & Data | 30 | 100% | 100% | 21-May-26 | 28-Jun-26 | 28-Jul-26 A | 28-Jul-26 A | 0.00 | 0.00 | 0.00 | -26 |
| MLTX-02-005-EN-1 | Approval of Method Statement for CCTV System | 30 | 100% | 100% | 21-May-26 | 28-Jun-26 | 28-Jul-26 A | 28-Jul-26 A | 0.00 | 0.00 | 0.00 | -26 |
| MLTX-02-005-EN-1 | Approval of Method Statement for Lighting Works | 21 | 100% | 100% | 30-Apr-26 | 24-May-26 | 14-Jul-26 A | 14-Jul-26 A | 0.00 | 0.00 | 0.00 | -41 |
| MLTX-02-005-EN-1 | Approval of Method Statement for Earthing/Lightning Works | 21 | 100% | 100% | 30-Apr-26 | 24-May-26 | 14-Jul-26 A | 14-Jul-26 A | 0.00 | 0.00 | 0.00 | -41 |
| MLTX-02-005-EN-1 | Approval of Method Statement for Panel Boards Works | 21 | 100% | 100% | 30-Apr-26 | 24-May-26 | 14-Jul-26 A | 14-Jul-26 A | 0.00 | 0.00 | 0.00 | -41 |
| **PRE-QUALIFICATION & MATERIAL** | | 93 | 0% | 0% | 09-Mar-26 | 10-Jun-26 | 08-Mar-26 A | 12-Sep-26 A | 0.00 | 0.00 | 0.00 | -80 |
| **PRE-QUALIFICATION** | | 45 | 0% | 0% | 09-Mar-26 | 03-May-26 | 08-Mar-26 A | 07-Jun-26 A | 0.00 | 0.00 | 0.00 | -27 |
| **TOILET/SERVICE WORKS** | | 45 | 0% | 0% | 09-Mar-26 | 03-May-26 | 08-Mar-26 A | 07-Jun-26 A | 0.00 | 0.00 | 0.00 | -27 |
| **STEEL REINFORCEMENT** | | 30 | 0% | 0% | 09-Mar-26 | 15-Apr-26 | 09-Mar-26 A | 19-Mar-26 A | 0.00 | 0.00 | 0.00 | 20 |
| MLTX-02-005-EN | Pre-Qualification Submittal for Steel Reinforcement | 15 | 100% | 100% | 09-Mar-26 | 29-Mar-26 | 09-Mar-26 A | 11-Mar-26 A | 0.00 | 0.00 | 0.00 | 12 |
| MLTX-02-005-EN | Pre-Qualification Approval for Steel Reinforcement | 15 | 100% | 100% | 30-Mar-26 | 15-Apr-26 | 12-Mar-26 A | 19-Mar-26 A | 0.00 | 0.00 | 0.00 | 20 |
| **READY MIX CONCRETE** | | 30 | 0% | 0% | 09-Mar-26 | 15-Apr-26 | 09-Mar-26 A | 19-Mar-26 A | 0.00 | 0.00 | 0.00 | 20 |
| MLTX-02-005-EN | Pre-Qualification Submittal for Ready Mixed Concrete | 15 | 100% | 100% | 09-Mar-26 | 29-Mar-26 | 09-Mar-26 A | 11-Mar-26 A | 0.00 | 0.00 | 0.00 | 12 |
| MLTX-02-005-EN | Pre-Qualification Approval of Ready Mixed Concrete | 15 | 100% | 100% | 30-Mar-26 | 15-Apr-26 | 12-Mar-26 A | 19-Mar-26 A | 0.00 | 0.00 | 0.00 | 20 |
| **CONCRETE BLOCKS** | | 30 | 0% | 0% | 09-Mar-26 | 15-Apr-26 | 09-Mar-26 A | 19-Mar-26 A | 0.00 | 0.00 | 0.00 | 20 |
| MLTX-02-005-EN | Pre-Qualification Submittal for Concrete Blocks | 15 | 100% | 100% | 09-Mar-26 | 29-Mar-26 | 09-Mar-26 A | 11-Mar-26 A | 0.00 | 0.00 | 0.00 | 12 |
| MLTX-02-005-EN | Pre-Qualification Approval for Concrete Blocks | 15 | 100% | 100% | 30-Mar-26 | 15-Apr-26 | 12-Mar-26 A | 19-Mar-26 A | 0.00 | 0.00 | 0.00 | 20 |
| **WATER PROOFING** | | 36 | 0% | 0% | 09-Mar-26 | 22-Apr-26 | 09-Mar-26 A | 19-Mar-26 A | 0.00 | 0.00 | 0.00 | 26 |
| MLTX-02-005-EN | Pre-Qualification Submittal for Water Proofing | 15 | 100% | 100% | 09-Mar-26 | 29-Mar-26 | 09-Mar-26 A | 11-Mar-26 A | 0.00 | 0.00 | 0.00 | 12 |
| MLTX-02-005-EN | Pre-Qualification Approval for Water Proofing | 21 | 100% | 100% | 30-Mar-26 | 22-Apr-26 | 12-Mar-26 A | 19-Mar-26 A | 0.00 | 0.00 | 0.00 | 26 |
| **FLOOR/WALL TILES** | | 30 | 0% | 0% | 09-Mar-26 | 15-Apr-26 | 08-Mar-26 A | 10-May-26 A | 0.00 | 0.00 | 0.00 | -21 |
| MLTX-02-005-EN | Pre-Qualification Submittal for Tilling Materials | 15 | 100% | 100% | 09-Mar-26 | 29-Mar-26 | 08-Mar-26 A | 06-May-26 A | 0.00 | 0.00 | 0.00 | -33 |
| MLTX-02-005-EN | Pre-Qualification Approval for Tailling Material | 15 | 100% | 100% | 30-Mar-26 | 15-Apr-26 | 11-Mar-26 A | 10-May-26 A | 0.00 | 0.00 | 0.00 | -21 |
| **SUSPENDED CEILING** | | 30 | 0% | 0% | 09-Mar-26 | 15-Apr-26 | 09-Mar-26 A | 19-Mar-26 A | 0.00 | 0.00 | 0.00 | 20 |

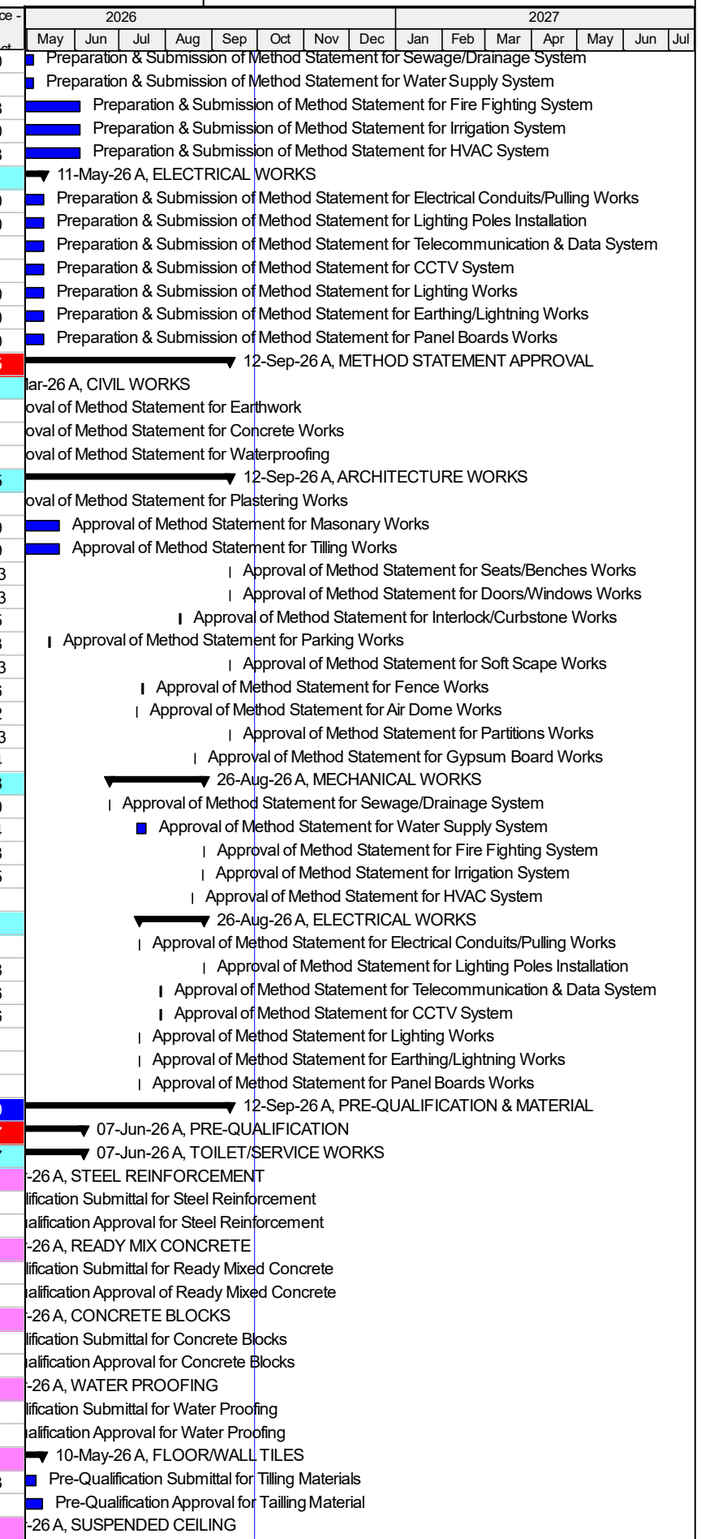


Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary




TASK filter: All Activities

© Oracle Corporation

# MLTX-02-005 - Playground Initiative for Eastern Region (Arar-Hasa osis -Dammam)

**Updateded schedule**
**D.D 28-09-2026**

| Activity ID | Activity Name | Original Duration | Schedule % Complete | Performance % Complete | BL Project Start | BL Project Finish | Start | Finish | Planned Value Cost | Earned Value Cost | Budgeted Total Cost | Variance - BL Project |
|---|---|---|---|---|---|---|---|---|---|---|---|---|
| MLTX-02-005-EN | Pre-Qualification Submittal for Suspend Ceiling | 15 | 100% | 100% | 09-Mar-26 | 29-Mar-26 | 09-Mar-26 A | 11-Mar-26 A | 0.00 | 0.00 | 0.00 | 12 |
| MLTX-02-005-EN | Pre-Qualification Approval for Suspend Ceiling | 15 | 100% | 100% | 30-Mar-26 | 15-Apr-26 | 12-Mar-26 A | 19-Mar-26 A | 0.00 | 0.00 | 0.00 | 20 |
| **DOORS/WINDOWS** | | 30 | 0% | 0% | 09-Mar-26 | 15-Apr-26 | 09-Mar-26 A | 19-Mar-26 A | 0.00 | 0.00 | 0.00 | 20 |
| MLTX-02-005-EN | Pre-Qualification Submittal for Doors/Windows | 15 | 100% | 100% | 09-Mar-26 | 29-Mar-26 | 09-Mar-26 A | 11-Mar-26 A | 0.00 | 0.00 | 0.00 | 12 |
| MLTX-02-005-EN | Pre-Qualification Approval for Doors/Windows | 15 | 100% | 100% | 30-Mar-26 | 15-Apr-26 | 12-Mar-26 A | 19-Mar-26 A | 0.00 | 0.00 | 0.00 | 20 |
| **FURNITURES** | | 30 | 0% | 0% | 09-Mar-26 | 15-Apr-26 | 08-Mar-26 A | 12-May-26 A | 0.00 | 0.00 | 0.00 | -23 |
| MLTX-02-005-EN | Pre-Qualification Submittal for Furnitures | 15 | 100% | 100% | 09-Mar-26 | 29-Mar-26 | 08-Mar-26 A | 07-May-26 A | 0.00 | 0.00 | 0.00 | -34 |
| MLTX-02-005-EN | Pre-Qualification Approval for Furnitures | 15 | 100% | 100% | 30-Mar-26 | 15-Apr-26 | 11-Mar-26 A | 12-May-26 A | 0.00 | 0.00 | 0.00 | -23 |
| **SANITARY FIXTURES** | | 30 | 0% | 0% | 09-Mar-26 | 15-Apr-26 | 08-Mar-26 A | 10-May-26 A | 0.00 | 0.00 | 0.00 | -21 |
| MLTX-02-005-EN | Pre-Qualification Submittal for Sanitary Fixtures | 15 | 100% | 100% | 09-Mar-26 | 29-Mar-26 | 08-Mar-26 A | 06-May-26 A | 0.00 | 0.00 | 0.00 | -33 |
| MLTX-02-005-EN | Pre-Qualification Approval for Sanitary Fixtures | 15 | 100% | 100% | 30-Mar-26 | 15-Apr-26 | 11-Mar-26 A | 10-May-26 A | 0.00 | 0.00 | 0.00 | -21 |
| **WATER SUPPLY PIPES** | | 30 | 0% | 0% | 09-Mar-26 | 15-Apr-26 | 08-Mar-26 A | 07-Jun-26 A | 0.00 | 0.00 | 0.00 | -42 |
| MLTX-02-005-EN | Pre-Qualification Submittal for Water Supply Pipes | 15 | 100% | 100% | 09-Mar-26 | 29-Mar-26 | 08-Mar-26 A | 25-May-26 A | 0.00 | 0.00 | 0.00 | -49 |
| MLTX-02-005-EN | Pre-Qualification Approval for Water Supply Pipes | 15 | 100% | 100% | 30-Mar-26 | 15-Apr-26 | 11-Mar-26 A | 07-Jun-26 A | 0.00 | 0.00 | 0.00 | -42 |
| **SEWAGE/DRAINAGE PIPES** | | 30 | 0% | 0% | 09-Mar-26 | 15-Apr-26 | 08-Mar-26 A | 07-Jun-26 A | 0.00 | 0.00 | 0.00 | -42 |
| MLTX-02-005-EN | Pre-Qualification Submittal for Sewage/Drainage Pipes | 15 | 100% | 100% | 09-Mar-26 | 29-Mar-26 | 08-Mar-26 A | 25-May-26 A | 0.00 | 0.00 | 0.00 | -49 |
| MLTX-02-005-EN | Pre-Qualification Approval for Sewage/Drainage Pipes | 15 | 100% | 100% | 30-Mar-26 | 15-Apr-26 | 11-Mar-26 A | 07-Jun-26 A | 0.00 | 0.00 | 0.00 | -42 |
| **PACKAGE AC UNITS** | | 30 | 0% | 0% | 30-Mar-26 | 03-May-26 | 11-Mar-26 A | 07-Jun-26 A | 0.00 | 0.00 | 0.00 | -27 |
| MLTX-02-005-EN | Pre-Qualification Submittal for Package AC Units | 15 | 100% | 100% | 30-Mar-26 | 15-Apr-26 | 11-Mar-26 A | 25-May-26 A | 0.00 | 0.00 | 0.00 | -34 |
| MLTX-02-005-EN | Pre-Qualification Approval for Package AC Units | 15 | 100% | 100% | 16-Apr-26 | 03-May-26 | 15-Mar-26 A | 07-Jun-26 A | 0.00 | 0.00 | 0.00 | -27 |
| **AIR DIFUSSERS/GRILLS** | | 30 | 0% | 0% | 30-Mar-26 | 03-May-26 | 11-Mar-26 A | 07-Jun-26 A | 0.00 | 0.00 | 0.00 | -27 |
| MLTX-02-005-EN | Pre-Qualification Submittal for Air Diffusers/Grills | 15 | 100% | 100% | 30-Mar-26 | 15-Apr-26 | 11-Mar-26 A | 25-May-26 A | 0.00 | 0.00 | 0.00 | -34 |
| MLTX-02-005-EN | Pre-Qualification Approval for Air Diffusers/Grills | 15 | 100% | 100% | 16-Apr-26 | 03-May-26 | 15-Mar-26 A | 07-Jun-26 A | 0.00 | 0.00 | 0.00 | -27 |
| **GALVANIZED DUCTS** | | 30 | 0% | 0% | 30-Mar-26 | 03-May-26 | 11-Mar-26 A | 30-Apr-26 A | 0.00 | 0.00 | 0.00 | 2 |
| MLTX-02-005-EN | Pre-Qualification Submittal for Galvanized Ducts | 15 | 100% | 100% | 30-Mar-26 | 15-Apr-26 | 11-Mar-26 A | 25-Apr-26 A | 0.00 | 0.00 | 0.00 | -8 |
| MLTX-02-005-EN | Pre-Qualification Approval for Galvanized Ducts | 15 | 100% | 100% | 16-Apr-26 | 03-May-26 | 15-Mar-26 A | 30-Apr-26 A | 0.00 | 0.00 | 0.00 | 2 |
| **EXHAUST FANS** | | 30 | 0% | 0% | 30-Mar-26 | 03-May-26 | 11-Mar-26 A | 07-Jun-26 A | 0.00 | 0.00 | 0.00 | -27 |
| MLTX-02-005-EN | Pre-Qualification Submittal for Exhaust Fans | 15 | 100% | 100% | 30-Mar-26 | 15-Apr-26 | 11-Mar-26 A | 25-May-26 A | 0.00 | 0.00 | 0.00 | -34 |
| MLTX-02-005-EN | Pre-Qualification Approval for Exhaust Fans | 15 | 100% | 100% | 16-Apr-26 | 03-May-26 | 15-Mar-26 A | 07-Jun-26 A | 0.00 | 0.00 | 0.00 | -27 |
| **LIGHTING FIXTURES** | | 30 | 0% | 0% | 30-Mar-26 | 03-May-26 | 11-Mar-26 A | 07-Jun-26 A | 0.00 | 0.00 | 0.00 | -27 |
| MLTX-02-005-EN | Pre-Qualification Submittal for Lighting Fixtures | 15 | 100% | 100% | 30-Mar-26 | 15-Apr-26 | 11-Mar-26 A | 25-May-26 A | 0.00 | 0.00 | 0.00 | -34 |
| MLTX-02-005-EN | Pre-Qualification Approval for Lighting Fixtures | 15 | 100% | 100% | 16-Apr-26 | 03-May-26 | 15-Mar-26 A | 07-Jun-26 A | 0.00 | 0.00 | 0.00 | -27 |
| **SWITCHES/SOCKETS** | | 30 | 0% | 0% | 30-Mar-26 | 03-May-26 | 11-Mar-26 A | 07-Jun-26 A | 0.00 | 0.00 | 0.00 | -27 |
| MLTX-02-005-EN | Pre-Qualification Submittal for Switches/Sockets | 15 | 100% | 100% | 30-Mar-26 | 15-Apr-26 | 11-Mar-26 A | 25-May-26 A | 0.00 | 0.00 | 0.00 | -34 |
| MLTX-02-005-EN | Pre-Qualification Approval for Switches/Sockets | 15 | 100% | 100% | 16-Apr-26 | 03-May-26 | 15-Mar-26 A | 07-Jun-26 A | 0.00 | 0.00 | 0.00 | -27 |
| **EARTHING SYSTEM** | | 30 | 0% | 0% | 30-Mar-26 | 03-May-26 | 11-Mar-26 A | 11-May-26 A | 0.00 | 0.00 | 0.00 | -7 |
| MLTX-02-005-EN | Pre-Qualification Submittal for Earthing System | 15 | 100% | 100% | 30-Mar-26 | 15-Apr-26 | 11-Mar-26 A | 09-May-26 A | 0.00 | 0.00 | 0.00 | -20 |
| MLTX-02-005-EN | Pre-Qualification Approval for Earthing System | 15 | 100% | 100% | 16-Apr-26 | 03-May-26 | 15-Mar-26 A | 11-May-26 A | 0.00 | 0.00 | 0.00 | -7 |
| **DISTRIBUTION PANNELS** | | 30 | 0% | 0% | 30-Mar-26 | 03-May-26 | 11-Mar-26 A | 07-Jun-26 A | 0.00 | 0.00 | 0.00 | -27 |
| MLTX-02-005-EN | Pre-Qualification Submittal for Distribution Panels | 15 | 100% | 100% | 30-Mar-26 | 15-Apr-26 | 11-Mar-26 A | 25-May-26 A | 0.00 | 0.00 | 0.00 | -34 |
| MLTX-02-005-EN | Pre-Qualification Approval for Distribution Panels | 15 | 100% | 100% | 16-Apr-26 | 03-May-26 | 15-Mar-26 A | 07-Jun-26 A | 0.00 | 0.00 | 0.00 | -27 |
| **PLAYGROUND WORKS** | | 45 | 0% | 0% | 09-Mar-26 | 03-May-26 | 08-Mar-26 A | 07-Jun-26 A | 0.00 | 0.00 | 0.00 | -27 |
| **PVC MEMBRANE** | | 30 | 0% | 0% | 09-Mar-26 | 15-Apr-26 | 08-Mar-26 A | 24-May-26 A | 0.00 | 0.00 | 0.00 | -33 |
| MLTX-02-005-EN | Pre-Qualification Submittal for PVC Membrane | 15 | 100% | 100% | 09-Mar-26 | 29-Mar-26 | 08-Mar-26 A | 20-May-26 A | 0.00 | 0.00 | 0.00 | -45 |
| MLTX-02-005-EN | Pre-Qualification Approval for PVC Membrane | 15 | 100% | 100% | 30-Mar-26 | 15-Apr-26 | 11-Mar-26 A | 24-May-26 A | 0.00 | 0.00 | 0.00 | -33 |
| **STEEL TENSION CABLES** | | 30 | 0% | 0% | 09-Mar-26 | 15-Apr-26 | 08-Mar-26 A | 24-May-26 A | 0.00 | 0.00 | 0.00 | -33 |
| MLTX-02-005-EN | Pre-Qualification Submittal for Steel Tension Cables | 15 | 100% | 100% | 09-Mar-26 | 29-Mar-26 | 08-Mar-26 A | 20-May-26 A | 0.00 | 0.00 | 0.00 | -45 |
| MLTX-02-005-EN | Pre-Qualification Approval for Steel Tension Cables | 15 | 100% | 100% | 30-Mar-26 | 15-Apr-26 | 11-Mar-26 A | 24-May-26 A | 0.00 | 0.00 | 0.00 | -33 |
| **EMERGENCY DOORS** | | 30 | 0% | 0% | 09-Mar-26 | 15-Apr-26 | 08-Mar-26 A | 24-May-26 A | 0.00 | 0.00 | 0.00 | -33 |
| MLTX-02-005-EN | Pre-Qualification Submittal for Emergency Doors | 15 | 100% | 100% | 09-Mar-26 | 29-Mar-26 | 08-Mar-26 A | 20-May-26 A | 0.00 | 0.00 | 0.00 | -45 |
| MLTX-02-005-EN | Pre-Qualification Approval for Emergency Doors | 15 | 100% | 100% | 30-Mar-26 | 15-Apr-26 | 11-Mar-26 A | 24-May-26 A | 0.00 | 0.00 | 0.00 | -33 |
| **PRESSURE UNITS** | | 30 | 0% | 0% | 09-Mar-26 | 15-Apr-26 | 08-Mar-26 A | 24-May-26 A | 0.00 | 0.00 | 0.00 | -33 |
| MLTX-02-005-EN | Pre-Qualification Submittal for Pressure Units | 15 | 100% | 100% | 09-Mar-26 | 29-Mar-26 | 08-Mar-26 A | 20-May-26 A | 0.00 | 0.00 | 0.00 | -45 |
| MLTX-02-005-EN | Pre-Qualification Approval for Pressure Units | 15 | 100% | 100% | 30-Mar-26 | 15-Apr-26 | 11-Mar-26 A | 24-May-26 A | 0.00 | 0.00 | 0.00 | -33 |
| **AIR LOCK DOORS** | | 30 | 0% | 0% | 09-Mar-26 | 15-Apr-26 | 08-Mar-26 A | 24-May-26 A | 0.00 | 0.00 | 0.00 | -33 |
| MLTX-02-005-EN | Pre-Qualification Submittal for Lock Doors | 15 | 100% | 100% | 09-Mar-26 | 29-Mar-26 | 08-Mar-26 A | 20-May-26 A | 0.00 | 0.00 | 0.00 | -45 |
| MLTX-02-005-EN | Pre-Qualification Approval for Lock Doors | 15 | 100% | 100% | 30-Mar-26 | 15-Apr-26 | 11-Mar-26 A | 24-May-26 A | 0.00 | 0.00 | 0.00 | -33 |
| **ARTIFICIAL TURF** | | 30 | 0% | 0% | 09-Mar-26 | 15-Apr-26 | 08-Mar-26 A | 10-May-26 A | 0.00 | 0.00 | 0.00 | -21 |
| MLTX-02-005-EN | Pre-Qualification Submittal for Artificial TURF | 15 | 100% | 100% | 09-Mar-26 | 29-Mar-26 | 08-Mar-26 A | 06-May-26 A | 0.00 | 0.00 | 0.00 | -33 |
| MLTX-02-005-EN | Pre-Qualification Approval for Artificial TURF | 15 | 100% | 100% | 30-Mar-26 | 15-Apr-26 | 11-Mar-26 A | 10-May-26 A | 0.00 | 0.00 | 0.00 | -21 |
| **RUBBER GRANULES** | | 30 | 0% | 0% | 09-Mar-26 | 15-Apr-26 | 08-Mar-26 A | 11-May-26 A | 0.00 | 0.00 | 0.00 | -22 |
| MLTX-02-005-EN | Pre-Qualification Submittal for Rubber Granules | 15 | 100% | 100% | 09-Mar-26 | 29-Mar-26 | 08-Mar-26 A | 06-May-26 A | 0.00 | 0.00 | 0.00 | -33 |
| MLTX-02-005-EN | Pre-Qualification Approval for Rubber Granules | 15 | 100% | 100% | 30-Mar-26 | 15-Apr-26 | 11-Mar-26 A | 11-May-26 A | 0.00 | 0.00 | 0.00 | -22 |
| **PADEL GLASS** | | 30 | 0% | 0% | 09-Mar-26 | 15-Apr-26 | 08-Mar-26 A | 11-May-26 A | 0.00 | 0.00 | 0.00 | -22 |

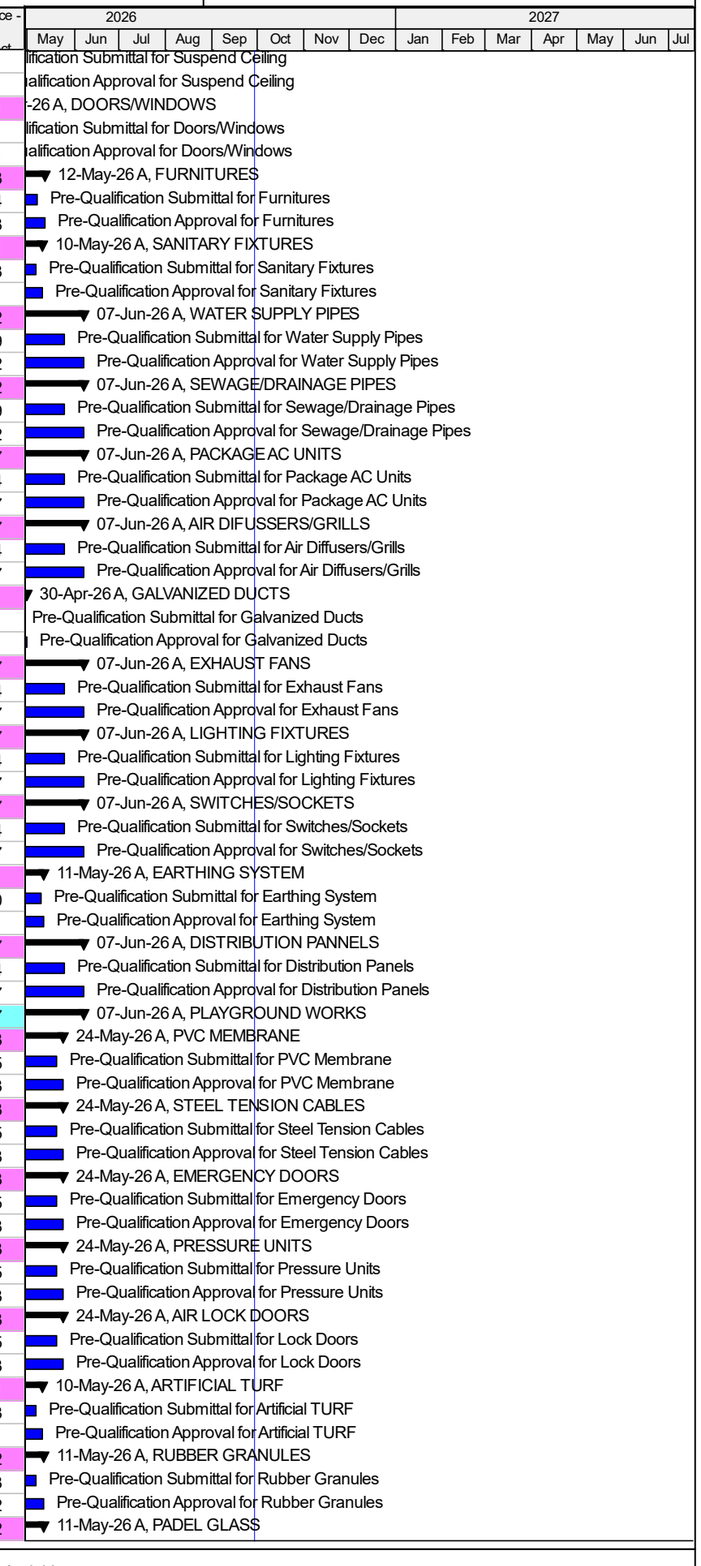


Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary




TASK filter: All Activities

© Oracle Corporation

# MLTX-02-005 - Playground Initiative for Eastern Region (Arar-Hasa osis -Dammam)

**Updateded schedule**
**D.D 28-09-2026**

| Activity ID | Activity Name | Original Duration | Schedule % Complete | Performance % Complete | BL Project Start | BL Project Finish | Start | Finish | Planned Value Cost | Earned Value Cost | Budgeted Total Cost | Variance - BL Project |
|---|---|---|---|---|---|---|---|---|---|---|---|---|
| MLTX-02-005-EN | Pre-Qualification Submittal for Padel Glass | 15 | 100% | 100% | 09-Mar-26 | 29-Mar-26 | 08-Mar-26 A | 06-May-26 A | 0.00 | 0.00 | 0.00 | -33 |
| MLTX-02-005-EN | Pre-Qualification Approval for Padel Glass | 15 | 100% | 100% | 30-Mar-26 | 15-Apr-26 | 11-Mar-26 A | 11-May-26 A | 0.00 | 0.00 | 0.00 | -22 |
| **PADEL WIRE MESH/STEEL SETS** | | 30 | 0% | 0% | 09-Mar-26 | 15-Apr-26 | 08-Mar-26 A | 11-May-26 A | 0.00 | 0.00 | 0.00 | -22 |
| MLTX-02-005-EN | Pre-Qualification Submittal for Wire Mesh/Steel Sets | 15 | 100% | 100% | 09-Mar-26 | 29-Mar-26 | 08-Mar-26 A | 06-May-26 A | 0.00 | 0.00 | 0.00 | -33 |
| MLTX-02-005-EN | Pre-Qualification Approval for Wire Mesh/Steel Sets | 15 | 100% | 100% | 30-Mar-26 | 15-Apr-26 | 11-Mar-26 A | 11-May-26 A | 0.00 | 0.00 | 0.00 | -22 |
| **AGGREGATE BASE COURSE** | | 30 | 0% | 0% | 09-Mar-26 | 15-Apr-26 | 08-Mar-26 A | 30-Apr-26 A | 0.00 | 0.00 | 0.00 | -13 |
| MLTX-02-005-EN | Pre-Qualification Submittal for Aggregate Base Course | 15 | 100% | 100% | 09-Mar-26 | 29-Mar-26 | 08-Mar-26 A | 26-Apr-26 A | 0.00 | 0.00 | 0.00 | -24 |
| MLTX-02-005-EN | Pre-Qualification Approval for Aggregate Base Course | 15 | 100% | 100% | 30-Mar-26 | 15-Apr-26 | 11-Mar-26 A | 30-Apr-26 A | 0.00 | 0.00 | 0.00 | -13 |
| **BITUMINOUS BASE & WEARING COURSE** | | 30 | 0% | 0% | 30-Mar-26 | 03-May-26 | 11-Mar-26 A | 30-Apr-26 A | 0.00 | 0.00 | 0.00 | 2 |
| MLTX-02-005-EN | Pre-Qualification Submittal for Bituminous Base & Wearing | 15 | 100% | 100% | 30-Mar-26 | 15-Apr-26 | 11-Mar-26 A | 26-Apr-26 A | 0.00 | 0.00 | 0.00 | -9 |
| MLTX-02-005-EN | Pre-Qualification Approval for the Site | 15 | 100% | 100% | 16-Apr-26 | 03-May-26 | 15-Mar-26 A | 30-Apr-26 A | 0.00 | 0.00 | 0.00 | 2 |
| **INTERLOCKING PAVING** | | 30 | 0% | 0% | 30-Mar-26 | 03-May-26 | 11-Mar-26 A | 04-May-26 A | 0.00 | 0.00 | 0.00 | -1 |
| MLTX-02-005-EN | Pre-Qualification Submittal for Interlocking Block Pavers | 15 | 100% | 100% | 30-Mar-26 | 15-Apr-26 | 11-Mar-26 A | 30-Apr-26 A | 0.00 | 0.00 | 0.00 | -13 |
| MLTX-02-005-EN | Pre-Qualification Approval for Interlocking Block Pavers | 15 | 100% | 100% | 16-Apr-26 | 03-May-26 | 15-Mar-26 A | 04-May-26 A | 0.00 | 0.00 | 0.00 | -1 |
| **MARKING PAINT** | | 30 | 0% | 0% | 30-Mar-26 | 03-May-26 | 11-Mar-26 A | 09-May-26 A | 0.00 | 0.00 | 0.00 | -5 |
| MLTX-02-005-EN | Pre-Qualification Submittal for Marking Paint | 15 | 100% | 100% | 30-Mar-26 | 15-Apr-26 | 11-Mar-26 A | 05-May-26 A | 0.00 | 0.00 | 0.00 | -17 |
| MLTX-02-005-EN | Pre-Qualification Approval for Marking Paint | 15 | 100% | 100% | 16-Apr-26 | 03-May-26 | 15-Mar-26 A | 09-May-26 A | 0.00 | 0.00 | 0.00 | -5 |
| **PACKAGE AC UNITS** | | 30 | 0% | 0% | 30-Mar-26 | 03-May-26 | 11-Mar-26 A | 07-Jun-26 A | 0.00 | 0.00 | 0.00 | -27 |
| MLTX-02-005-EN | Pre-Qualification Submittal for Package AC Units | 15 | 100% | 100% | 30-Mar-26 | 15-Apr-26 | 11-Mar-26 A | 25-May-26 A | 0.00 | 0.00 | 0.00 | -34 |
| MLTX-02-005-EN | Pre-Qualification Approval for Package AC Units | 15 | 100% | 100% | 16-Apr-26 | 03-May-26 | 15-Mar-26 A | 07-Jun-26 A | 0.00 | 0.00 | 0.00 | -27 |
| **AIR DIFUSSERS/GRILLS** | | 30 | 0% | 0% | 30-Mar-26 | 03-May-26 | 11-Mar-26 A | 07-Jun-26 A | 0.00 | 0.00 | 0.00 | -27 |
| MLTX-02-005-EN | Pre-Qualification Submittal for Air Difussers/Grills | 15 | 100% | 100% | 30-Mar-26 | 15-Apr-26 | 11-Mar-26 A | 25-May-26 A | 0.00 | 0.00 | 0.00 | -34 |
| MLTX-02-005-EN | Pre-Qualification Approval for Air Difussers/Grills | 15 | 100% | 100% | 16-Apr-26 | 03-May-26 | 15-Mar-26 A | 07-Jun-26 A | 0.00 | 0.00 | 0.00 | -27 |
| **GALVANIZED DUCTS** | | 30 | 0% | 0% | 30-Mar-26 | 03-May-26 | 11-Mar-26 A | 30-Apr-26 A | 0.00 | 0.00 | 0.00 | 2 |
| MLTX-02-005-EN | Pre-Qualification Submittal for Galvanized Duct | 15 | 100% | 100% | 30-Mar-26 | 15-Apr-26 | 11-Mar-26 A | 25-Apr-26 A | 0.00 | 0.00 | 0.00 | -8 |
| MLTX-02-005-EN | Pre-Qualification Approval for Galvanized Duct | 15 | 100% | 100% | 16-Apr-26 | 03-May-26 | 15-Mar-26 A | 30-Apr-26 A | 0.00 | 0.00 | 0.00 | 2 |
| **EXHAUST FANS** | | 30 | 0% | 0% | 30-Mar-26 | 03-May-26 | 11-Mar-26 A | 07-Jun-26 A | 0.00 | 0.00 | 0.00 | -27 |
| MLTX-02-005-EN | Pre-Qualification Submittal for Exhaust Fans | 15 | 100% | 100% | 30-Mar-26 | 15-Apr-26 | 11-Mar-26 A | 25-May-26 A | 0.00 | 0.00 | 0.00 | -34 |
| MLTX-02-005-EN | Pre-Qualification Approval for Exhaust Fans | 15 | 100% | 100% | 16-Apr-26 | 03-May-26 | 15-Mar-26 A | 07-Jun-26 A | 0.00 | 0.00 | 0.00 | -27 |
| **DISTRIBUTION BOARDS** | | 30 | 0% | 0% | 30-Mar-26 | 03-May-26 | 11-Mar-26 A | 07-Jun-26 A | 0.00 | 0.00 | 0.00 | -27 |
| MLTX-02-005-EN | Pre-Qualification Submittal for Distribution Boards | 15 | 100% | 100% | 30-Mar-26 | 15-Apr-26 | 11-Mar-26 A | 25-May-26 A | 0.00 | 0.00 | 0.00 | -34 |
| MLTX-02-005-EN | Pre-Qualification Approval for Distribution Boards | 15 | 100% | 100% | 16-Apr-26 | 03-May-26 | 15-Mar-26 A | 07-Jun-26 A | 0.00 | 0.00 | 0.00 | -27 |
| **POWER CABLES** | | 30 | 0% | 0% | 30-Mar-26 | 03-May-26 | 11-Mar-26 A | 11-May-26 A | 0.00 | 0.00 | 0.00 | -7 |
| MLTX-02-005-EN | Pre-Qualification Submittal for Power Cables | 15 | 100% | 100% | 30-Mar-26 | 15-Apr-26 | 11-Mar-26 A | 09-May-26 A | 0.00 | 0.00 | 0.00 | -20 |
| MLTX-02-005-EN | Pre-Qualification Approval for Power Cables | 15 | 100% | 100% | 16-Apr-26 | 03-May-26 | 15-Mar-26 A | 11-May-26 A | 0.00 | 0.00 | 0.00 | -7 |
| **LIGHT FIXTURES** | | 30 | 0% | 0% | 30-Mar-26 | 03-May-26 | 11-Mar-26 A | 07-Jun-26 A | 0.00 | 0.00 | 0.00 | -27 |
| MLTX-02-005-EN | Pre-Qualification Submittal for Light Fixtures | 15 | 100% | 100% | 30-Mar-26 | 15-Apr-26 | 11-Mar-26 A | 25-May-26 A | 0.00 | 0.00 | 0.00 | -34 |
| MLTX-02-005-EN | Pre-Qualification Approval for Light Fixtures | 15 | 100% | 100% | 16-Apr-26 | 03-May-26 | 15-Mar-26 A | 07-Jun-26 A | 0.00 | 0.00 | 0.00 | -27 |
| **CCTV MATERIALS** | | 30 | 0% | 0% | 30-Mar-26 | 03-May-26 | 11-Mar-26 A | 07-Jun-26 A | 0.00 | 0.00 | 0.00 | -27 |
| MLTX-02-005-EN | Pre-Qualification Submittal for CCTV | 15 | 100% | 100% | 30-Mar-26 | 15-Apr-26 | 11-Mar-26 A | 25-May-26 A | 0.00 | 0.00 | 0.00 | -34 |
| MLTX-02-005-EN | Pre-Qualification Approval for CCTV | 15 | 100% | 100% | 16-Apr-26 | 03-May-26 | 15-Mar-26 A | 07-Jun-26 A | 0.00 | 0.00 | 0.00 | -27 |
| **POWER OUTLETS/SWITCHES** | | 30 | 0% | 0% | 30-Mar-26 | 03-May-26 | 11-Mar-26 A | 07-Jun-26 A | 0.00 | 0.00 | 0.00 | -27 |
| MLTX-02-005-EN | Pre-Qualification Submittal for Power Outlets/Switches | 15 | 100% | 100% | 30-Mar-26 | 15-Apr-26 | 11-Mar-26 A | 25-May-26 A | 0.00 | 0.00 | 0.00 | -34 |
| MLTX-02-005-EN | Pre-Qualification Approval for Power Outlets/Switches | 15 | 100% | 100% | 16-Apr-26 | 03-May-26 | 15-Mar-26 A | 07-Jun-26 A | 0.00 | 0.00 | 0.00 | -27 |
| **LANDSCAPE WORKS** | | 30 | 0% | 0% | 30-Mar-26 | 03-May-26 | 11-Mar-26 A | 21-May-26 A | 0.00 | 0.00 | 0.00 | -16 |
| **INTERLOCKING PAVING** | | 30 | 0% | 0% | 30-Mar-26 | 03-May-26 | 12-Mar-26 A | 24-Mar-26 A | 0.00 | 0.00 | 0.00 | 34 |
| MLTX-02-005-EN | Pre-Qualification Submittal for Interlocking Block Pavers | 15 | 100% | 100% | 30-Mar-26 | 15-Apr-26 | 12-Mar-26 A | 15-Mar-26 A | 0.00 | 0.00 | 0.00 | 24 |
| MLTX-02-005-EN | Pre-Qualification Approval for Interlocking Block Pavers | 15 | 100% | 100% | 16-Apr-26 | 03-May-26 | 16-Mar-26 A | 24-Mar-26 A | 0.00 | 0.00 | 0.00 | 34 |
| **CURBSTONE** | | 30 | 0% | 0% | 30-Mar-26 | 03-May-26 | 12-Mar-26 A | 24-Mar-26 A | 0.00 | 0.00 | 0.00 | 34 |
| MLTX-02-005-EN | Pre-Qualification Submittal for Curbstone | 15 | 100% | 100% | 30-Mar-26 | 15-Apr-26 | 12-Mar-26 A | 15-Mar-26 A | 0.00 | 0.00 | 0.00 | 24 |
| MLTX-02-005-EN | Pre-Qualification Approval for Curbstone | 15 | 100% | 100% | 16-Apr-26 | 03-May-26 | 16-Mar-26 A | 24-Mar-26 A | 0.00 | 0.00 | 0.00 | 34 |
| **PAVEMENT MARKING** | | 30 | 0% | 0% | 30-Mar-26 | 03-May-26 | 11-Mar-26 A | 09-May-26 A | 0.00 | 0.00 | 0.00 | -5 |
| MLTX-02-005-EN | Pre-Qualification Submittal for Pavement Markings | 15 | 100% | 100% | 30-Mar-26 | 15-Apr-26 | 11-Mar-26 A | 05-May-26 A | 0.00 | 0.00 | 0.00 | -17 |
| MLTX-02-005-EN | Pre-Qualification Approval for Pavement Markings | 15 | 100% | 100% | 16-Apr-26 | 03-May-26 | 15-Mar-26 A | 09-May-26 A | 0.00 | 0.00 | 0.00 | -5 |
| **TRAFFIC SIGNS** | | 30 | 0% | 0% | 30-Mar-26 | 03-May-26 | 11-Mar-26 A | 09-May-26 A | 0.00 | 0.00 | 0.00 | -5 |
| MLTX-02-005-EN | Pre-Qualification Submittal for Traffic Signs | 15 | 100% | 100% | 30-Mar-26 | 15-Apr-26 | 11-Mar-26 A | 05-May-26 A | 0.00 | 0.00 | 0.00 | -17 |
| MLTX-02-005-EN | Pre-Qualification Approval for Traffic Signs | 15 | 100% | 100% | 16-Apr-26 | 03-May-26 | 15-Mar-26 A | 09-May-26 A | 0.00 | 0.00 | 0.00 | -5 |
| **IRRIGATION PIPES/SPRINKLERS** | | 30 | 0% | 0% | 30-Mar-26 | 03-May-26 | 11-Mar-26 A | 21-May-26 A | 0.00 | 0.00 | 0.00 | -16 |
| MLTX-02-005-EN | Pre-Qualification Submittal for Irrigation Pipes/Sprinkles | 15 | 100% | 100% | 30-Mar-26 | 15-Apr-26 | 11-Mar-26 A | 20-May-26 A | 0.00 | 0.00 | 0.00 | -30 |
| MLTX-02-005-EN | Pre-Qualification Approval for Irrigation Pipes/Sprinkles | 15 | 100% | 100% | 16-Apr-26 | 03-May-26 | 15-Mar-26 A | 21-May-26 A | 0.00 | 0.00 | 0.00 | -16 |
| **AGRICULTURE SOIL** | | 30 | 0% | 0% | 30-Mar-26 | 03-May-26 | 11-Mar-26 A | 21-May-26 A | 0.00 | 0.00 | 0.00 | -16 |
| MLTX-02-005-EN | Pre-Qualification Submittal for Agriculture Soil | 15 | 100% | 100% | 30-Mar-26 | 15-Apr-26 | 11-Mar-26 A | 20-May-26 A | 0.00 | 0.00 | 0.00 | -30 |
| MLTX-02-005-EN | Pre-Qualification Approval for Agriculture Soil | 15 | 100% | 100% | 16-Apr-26 | 03-May-26 | 15-Mar-26 A | 21-May-26 A | 0.00 | 0.00 | 0.00 | -16 |
| **TRACK SURFACE** | | 30 | 0% | 0% | 30-Mar-26 | 03-May-26 | 11-Mar-26 A | 21-May-26 A | 0.00 | 0.00 | 0.00 | -16 |

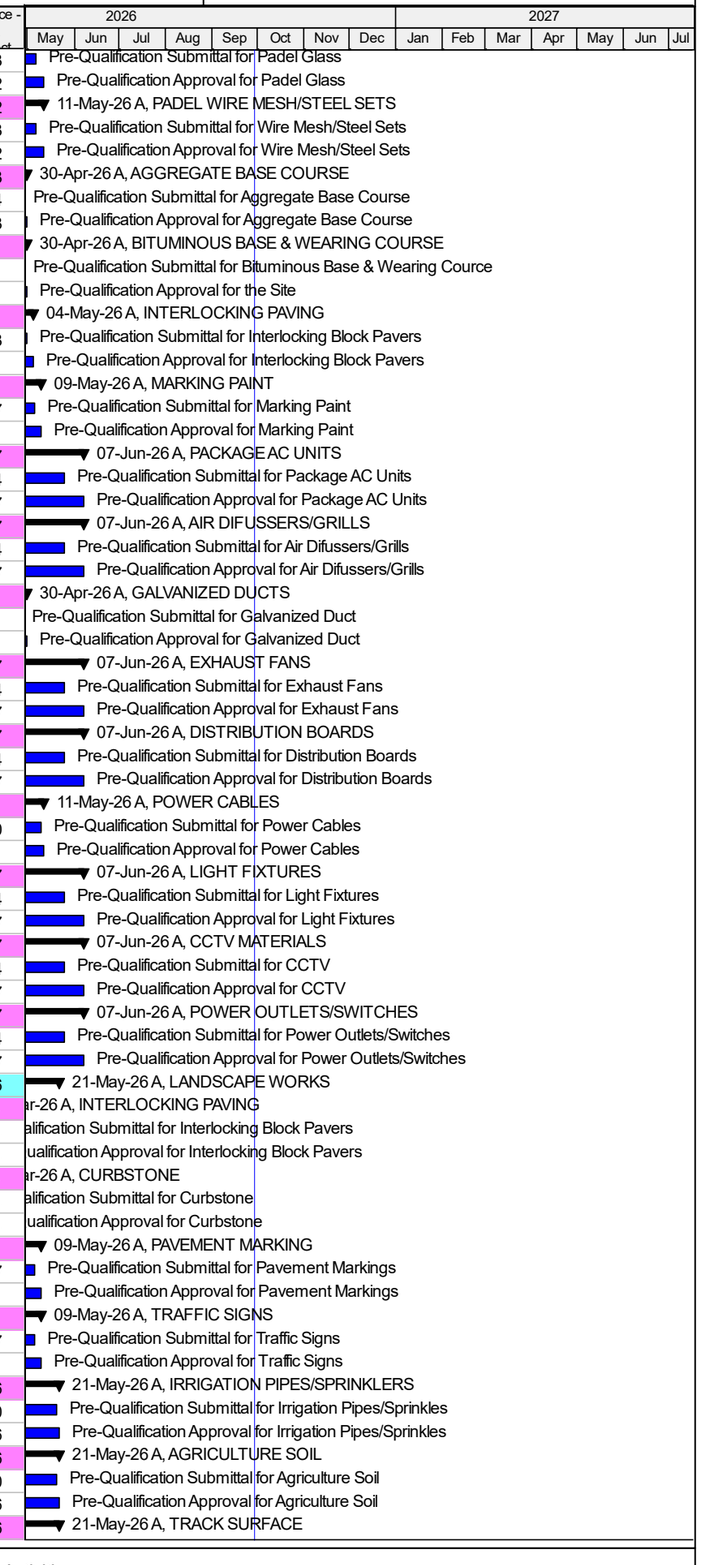


Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary



TASK filter: All Activities

© Oracle Corporation

# MLTX-02-005 - Playground Initiative for Eastern Region (Arar-Hasa osis -Dammam)

**Updateded schedule**
**D.D 28-09-2026**

| Activity ID | Activity Name | Original Duration | Schedule % Complete | Performance % Complete | BL Project Start | BL Project Finish | Start | Finish | Planned Value Cost | Earned Value Cost | Budgeted Total Cost | Variance - BL Project |
|---|---|---|---|---|---|---|---|---|---|---|---|---|
| MLTX-02-005-EN | Pre-Qualification Submittal for Track Surface | 15 | 100% | 100% | 30-Mar-26 | 15-Apr-26 | 11-Mar-26 A | 20-May-26 A | 0.00 | 0.00 | 0.00 | -30 |
| MLTX-02-005-EN | Pre-Qualification Approval for Track Surface | 15 | 100% | 100% | 16-Apr-26 | 03-May-26 | 15-Mar-26 A | 21-May-26 A | 0.00 | 0.00 | 0.00 | -16 |
| **GRASS/TREES** | | 30 | 0% | 0% | 30-Mar-26 | 03-May-26 | 11-Mar-26 A | 21-May-26 A | 0.00 | 0.00 | 0.00 | -16 |
| MLTX-02-005-EN | Pre-Qualification Submittal for Grass/Trees | 15 | 100% | 100% | 30-Mar-26 | 15-Apr-26 | 11-Mar-26 A | 20-May-26 A | 0.00 | 0.00 | 0.00 | -30 |
| MLTX-02-005-EN | Pre-Qualification Approval for Grass/Trees | 15 | 100% | 100% | 16-Apr-26 | 03-May-26 | 15-Mar-26 A | 21-May-26 A | 0.00 | 0.00 | 0.00 | -16 |
| **CABLES** | | 30 | 0% | 0% | 30-Mar-26 | 03-May-26 | 11-Mar-26 A | 11-May-26 A | 0.00 | 0.00 | 0.00 | -7 |
| MLTX-02-005-EN | Pre-Qualification Submittal for Cables | 15 | 100% | 100% | 30-Mar-26 | 15-Apr-26 | 11-Mar-26 A | 09-May-26 A | 0.00 | 0.00 | 0.00 | -20 |
| MLTX-02-005-EN | Pre-Qualification Approval for Cables | 15 | 100% | 100% | 16-Apr-26 | 03-May-26 | 15-Mar-26 A | 11-May-26 A | 0.00 | 0.00 | 0.00 | -7 |
| **LIGHT POLES** | | 30 | 0% | 0% | 30-Mar-26 | 03-May-26 | 11-Mar-26 A | 20-May-26 A | 0.00 | 0.00 | 0.00 | -15 |
| MLTX-02-005-EN | Pre-Qualification Submittal for Lighting poles | 15 | 100% | 100% | 30-Mar-26 | 15-Apr-26 | 11-Mar-26 A | 17-May-26 A | 0.00 | 0.00 | 0.00 | -27 |
| MLTX-02-005-EN | Pre-Qualification Approval for Lighting poles | 15 | 100% | 100% | 16-Apr-26 | 03-May-26 | 15-Mar-26 A | 20-May-26 A | 0.00 | 0.00 | 0.00 | -15 |
| **MATERIAL SUBMITTAL** | | 84 | 0% | 0% | 16-Apr-26 | 10-Jun-26 | 19-Mar-26 A | 12-Sep-26 A | 0.00 | 0.00 | 0.00 | -80 |
| **TOILET/SERVICE WORKS** | | 66 | 0% | 0% | 16-Apr-26 | 10-Jun-26 | 19-Mar-26 A | 30-Jul-26 A | 0.00 | 0.00 | 0.00 | -43 |
| **STEEL REINFORCEMENT** | | 30 | 0% | 0% | 16-Apr-26 | 20-May-26 | 19-Mar-26 A | 12-Apr-26 A | 0.00 | 0.00 | 0.00 | 33 |
| MLTX-02-005-EN | Material Submittal for Steel Reinforcement | 15 | 100% | 100% | 16-Apr-26 | 03-May-26 | 19-Mar-26 A | 07-Apr-26 A | 0.00 | 0.00 | 0.00 | 22 |
| MLTX-02-005-EN | Material Approval for Steel Reinforcement | 15 | 100% | 100% | 04-May-26 | 20-May-26 | 26-Mar-26 A | 12-Apr-26 A | 0.00 | 0.00 | 0.00 | 33 |
| **READY MIX CONCRETE** | | 30 | 0% | 0% | 16-Apr-26 | 20-May-26 | 19-Mar-26 A | 12-Apr-26 A | 0.00 | 0.00 | 0.00 | 33 |
| MLTX-02-005-EN | Material Submittal for Ready Mixed Concrete | 15 | 100% | 100% | 16-Apr-26 | 03-May-26 | 19-Mar-26 A | 07-Apr-26 A | 0.00 | 0.00 | 0.00 | 22 |
| MLTX-02-005-EN | Material Approval of Ready Mixed Concrete | 15 | 100% | 100% | 04-May-26 | 20-May-26 | 26-Mar-26 A | 12-Apr-26 A | 0.00 | 0.00 | 0.00 | 33 |
| **CONCRETE BLOCKS** | | 30 | 0% | 0% | 16-Apr-26 | 20-May-26 | 19-Mar-26 A | 11-May-26 A | 0.00 | 0.00 | 0.00 | 8 |
| MLTX-02-005-EN | Material Submittal for Concrete Blocks | 15 | 100% | 100% | 16-Apr-26 | 03-May-26 | 19-Mar-26 A | 06-May-26 A | 0.00 | 0.00 | 0.00 | -3 |
| MLTX-02-005-EN | Material Approval for Concrete Blocks | 15 | 100% | 100% | 04-May-26 | 20-May-26 | 26-Mar-26 A | 11-May-26 A | 0.00 | 0.00 | 0.00 | 8 |
| **FLOOR/WALL TILES** | | 30 | 0% | 0% | 16-Apr-26 | 20-May-26 | 19-Mar-26 A | 17-May-26 A | 0.00 | 0.00 | 0.00 | 3 |
| MLTX-02-005-EN | Material Submittal for Tilling Materials | 15 | 100% | 100% | 16-Apr-26 | 03-May-26 | 19-Mar-26 A | 13-May-26 A | 0.00 | 0.00 | 0.00 | -9 |
| MLTX-02-005-EN | Material Approval for Tilling Material | 15 | 100% | 100% | 04-May-26 | 20-May-26 | 26-Mar-26 A | 17-May-26 A | 0.00 | 0.00 | 0.00 | 3 |
| **SUSPENDED CEILING** | | 30 | 0% | 0% | 16-Apr-26 | 20-May-26 | 19-Mar-26 A | 13-May-26 A | 0.00 | 0.00 | 0.00 | 6 |
| MLTX-02-005-EN | Material Submittal for Suspend Ceiling | 15 | 100% | 100% | 16-Apr-26 | 03-May-26 | 19-Mar-26 A | 10-May-26 A | 0.00 | 0.00 | 0.00 | -6 |
| MLTX-02-005-EN | Material Approval for Suspend Ceiling | 15 | 100% | 100% | 04-May-26 | 20-May-26 | 26-Mar-26 A | 13-May-26 A | 0.00 | 0.00 | 0.00 | 6 |
| **DOORS/WINDOWS** | | 30 | 0% | 0% | 16-Apr-26 | 20-May-26 | 19-Mar-26 A | 12-May-26 A | 0.00 | 0.00 | 0.00 | 7 |
| MLTX-02-005-EN | Material Submittal for Doors/Windows | 15 | 100% | 100% | 16-Apr-26 | 03-May-26 | 19-Mar-26 A | 07-May-26 A | 0.00 | 0.00 | 0.00 | -4 |
| MLTX-02-005-EN | Material Approval for Doors/Windows | 15 | 100% | 100% | 04-May-26 | 20-May-26 | 26-Mar-26 A | 12-May-26 A | 0.00 | 0.00 | 0.00 | 7 |
| **FURNITURES** | | 30 | 0% | 0% | 16-Apr-26 | 20-May-26 | 19-Mar-26 A | 20-May-26 A | 0.00 | 0.00 | 0.00 | 0 |
| MLTX-02-005-EN | Material Submittal for Furnitures | 15 | 100% | 100% | 16-Apr-26 | 03-May-26 | 19-Mar-26 A | 14-May-26 A | 0.00 | 0.00 | 0.00 | -10 |
| MLTX-02-005-EN | Material Approval for Furnitures | 15 | 100% | 100% | 04-May-26 | 20-May-26 | 26-Mar-26 A | 20-May-26 A | 0.00 | 0.00 | 0.00 | 0 |
| **SANITARY FIXTURES** | | 30 | 0% | 0% | 16-Apr-26 | 20-May-26 | 19-Mar-26 A | 19-May-26 A | 0.00 | 0.00 | 0.00 | 1 |
| MLTX-02-005-EN | Material Submittal for Sanitary Fixtures | 15 | 100% | 100% | 16-Apr-26 | 03-May-26 | 19-Mar-26 A | 14-May-26 A | 0.00 | 0.00 | 0.00 | -10 |
| MLTX-02-005-EN | Material Approval for Sanitary Fixtures | 15 | 100% | 100% | 04-May-26 | 20-May-26 | 26-Mar-26 A | 19-May-26 A | 0.00 | 0.00 | 0.00 | 1 |
| **WATER SUPPLY PIPES** | | 30 | 0% | 0% | 16-Apr-26 | 20-May-26 | 19-Mar-26 A | 11-May-26 A | 0.00 | 0.00 | 0.00 | 8 |
| MLTX-02-005-EN | Material Submittal for Water Supply Pipes | 15 | 100% | 100% | 16-Apr-26 | 03-May-26 | 19-Mar-26 A | 06-May-26 A | 0.00 | 0.00 | 0.00 | -3 |
| MLTX-02-005-EN | Material Approval for Water Supply Pipes | 15 | 100% | 100% | 04-May-26 | 20-May-26 | 26-Mar-26 A | 11-May-26 A | 0.00 | 0.00 | 0.00 | 8 |
| **SEWAGE/DRAINAGE PIPES** | | 30 | 0% | 0% | 16-Apr-26 | 20-May-26 | 19-Mar-26 A | 11-May-26 A | 0.00 | 0.00 | 0.00 | 8 |
| MLTX-02-005-EN | Material Submittal for Sewage/Drainage Pipes | 15 | 100% | 100% | 16-Apr-26 | 03-May-26 | 19-Mar-26 A | 06-May-26 A | 0.00 | 0.00 | 0.00 | -3 |
| MLTX-02-005-EN | Material Approval for Sewage/Drainage Pipes | 15 | 100% | 100% | 04-May-26 | 20-May-26 | 26-Mar-26 A | 11-May-26 A | 0.00 | 0.00 | 0.00 | 8 |
| **PACKAGE AC UNITS** | | 30 | 0% | 0% | 04-May-26 | 10-Jun-26 | 07-Jul-26 A | 07-Jul-26 A | 0.00 | 0.00 | 0.00 | -23 |
| MLTX-02-005-EN | Material Submittal for Package AC Units | 15 | 100% | 100% | 04-May-26 | 20-May-26 | 07-Jul-26 A | 07-Jul-26 A | 0.00 | 0.00 | 0.00 | -38 |
| MLTX-02-005-EN | Material Approval for Package AC Units | 15 | 100% | 100% | 21-May-26 | 10-Jun-26 | 07-Jul-26 A | 07-Jul-26 A | 0.00 | 0.00 | 0.00 | -23 |
| **AIR DIFUSSERS/GRILLS** | | 30 | 0% | 0% | 04-May-26 | 10-Jun-26 | 28-Jul-26 A | 30-Jul-26 A | 0.00 | 0.00 | 0.00 | -43 |
| MLTX-02-005-EN | Material Submittal for Air Diffusers/Grills | 15 | 100% | 100% | 04-May-26 | 20-May-26 | 28-Jul-26 A | 28-Jul-26 A | 0.00 | 0.00 | 0.00 | -56 |
| MLTX-02-005-EN | Material Approval for Air Diffusers/Grills | 15 | 100% | 100% | 21-May-26 | 10-Jun-26 | 30-Jul-26 A | 30-Jul-26 A | 0.00 | 0.00 | 0.00 | -43 |
| **GALVANIZED DUCTS** | | 30 | 0% | 0% | 04-May-26 | 10-Jun-26 | 24-Mar-26 A | 30-Apr-26 A | 0.00 | 0.00 | 0.00 | 32 |
| MLTX-02-005-EN | Material Submittal for Galvanized Ducts | 15 | 100% | 100% | 04-May-26 | 20-May-26 | 24-Mar-26 A | 25-Apr-26 A | 0.00 | 0.00 | 0.00 | 22 |
| MLTX-02-005-EN | Material Approval for Galvanized Ducts | 15 | 100% | 100% | 21-May-26 | 10-Jun-26 | 28-Mar-26 A | 30-Apr-26 A | 0.00 | 0.00 | 0.00 | 32 |
| **EXHAUST FANS** | | 30 | 0% | 0% | 04-May-26 | 10-Jun-26 | 28-Jul-26 A | 30-Jul-26 A | 0.00 | 0.00 | 0.00 | -43 |
| MLTX-02-005-EN | Material Submittal for Exhaust Fans | 15 | 100% | 100% | 04-May-26 | 20-May-26 | 28-Jul-26 A | 28-Jul-26 A | 0.00 | 0.00 | 0.00 | -56 |
| MLTX-02-005-EN | Material Approval for Exhaust Fans | 15 | 100% | 100% | 21-May-26 | 10-Jun-26 | 30-Jul-26 A | 30-Jul-26 A | 0.00 | 0.00 | 0.00 | -43 |
| **LIGHTING FIXTURES** | | 30 | 0% | 0% | 04-May-26 | 10-Jun-26 | 07-Jul-26 A | 07-Jul-26 A | 0.00 | 0.00 | 0.00 | -23 |
| MLTX-02-005-EN | Material Submittal for Lighting Fixtures | 15 | 100% | 100% | 04-May-26 | 20-May-26 | 07-Jul-26 A | 07-Jul-26 A | 0.00 | 0.00 | 0.00 | -38 |
| MLTX-02-005-EN | Material Approval for Lighting Fixtures | 15 | 100% | 100% | 21-May-26 | 10-Jun-26 | 07-Jul-26 A | 07-Jul-26 A | 0.00 | 0.00 | 0.00 | -23 |
| **SWITCHES/SOCKETS** | | 30 | 0% | 0% | 04-May-26 | 10-Jun-26 | 28-Jul-26 A | 30-Jul-26 A | 0.00 | 0.00 | 0.00 | -43 |
| MLTX-02-005-EN | Material Submittal for Switches/Sockets | 15 | 100% | 100% | 04-May-26 | 20-May-26 | 28-Jul-26 A | 28-Jul-26 A | 0.00 | 0.00 | 0.00 | -56 |
| MLTX-02-005-EN | Material Approval for Switches/Sockets | 15 | 100% | 100% | 21-May-26 | 10-Jun-26 | 30-Jul-26 A | 30-Jul-26 A | 0.00 | 0.00 | 0.00 | -43 |
| **EARTHING SYSTEM** | | 30 | 0% | 0% | 04-May-26 | 10-Jun-26 | 24-Mar-26 A | 18-May-26 A | 0.00 | 0.00 | 0.00 | 17 |
| MLTX-02-005-EN | Material Submittal for Earthing System | 15 | 100% | 100% | 04-May-26 | 20-May-26 | 24-Mar-26 A | 14-May-26 A | 0.00 | 0.00 | 0.00 | 5 |
| MLTX-02-005-EN | Material Approval for Earthing System | 15 | 100% | 100% | 21-May-26 | 10-Jun-26 | 28-Mar-26 A | 18-May-26 A | 0.00 | 0.00 | 0.00 | 17 |




Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary



TASK filter: All Activities

© Oracle Corporation

# MLTX-02-005 - Playground Initiative for Eastern Region (Arar-Hasa osis -Dammam)


**Updateded schedule**
**D.D 28-09-2026**

PROFAST شركة برو فاست المحدودة

egis

MODON

| Activity ID | Activity Name | Original Duration | Schedule % Complete | Performance % Complete | BL Project Start | BL Project Finish | Start | Finish | Planned Value Cost | Earned Value Cost | Budgeted Total Cost | Variance - BL Project |
|---|---|---|---|---|---|---|---|---|---|---|---|---|
| **DISTRIBUTION PANNELS** | | 30 | 0% | 0% | 04-May-26 | 10-Jun-26 | 28-Jul-26 A | 30-Jul-26 A | 0.00 | 0.00 | 0.00 | -43 |
| MLTX-02-005-EI | Material Submittal for Distribution Panels | 15 | 100% | 100% | 04-May-26 | 20-May-26 | 28-Jul-26 A | 28-Jul-26 A | 0.00 | 0.00 | 0.00 | -56 |
| MLTX-02-005-EI | Material Approval for Distribution Panels | 15 | 100% | 100% | 21-May-26 | 10-Jun-26 | 30-Jul-26 A | 30-Jul-26 A | 0.00 | 0.00 | 0.00 | -43 |
| **PLAYGROUND WORKS** | | 84 | 0% | 0% | 16-Apr-26 | 10-Jun-26 | 19-Mar-26 A | 12-Sep-26 A | 0.00 | 0.00 | 0.00 | -80 |
| **PVC MEMBRANE** | | 30 | 0% | 0% | 16-Apr-26 | 20-May-26 | 26-Aug-26 A | 26-Aug-26 A | 0.00 | 0.00 | 0.00 | -81 |
| MLTX-02-005-EI | Material Submittal for PVC Membrane | 15 | 100% | 100% | 16-Apr-26 | 03-May-26 | 26-Aug-26 A | 26-Aug-26 A | 0.00 | 0.00 | 0.00 | -96 |
| MLTX-02-005-EI | Material Approval for PVC Membrane | 15 | 100% | 100% | 04-May-26 | 20-May-26 | 26-Aug-26 A | 26-Aug-26 A | 0.00 | 0.00 | 0.00 | -81 |
| **STEEL TENSION CABLES** | | 30 | 0% | 0% | 16-Apr-26 | 20-May-26 | 26-Aug-26 A | 26-Aug-26 A | 0.00 | 0.00 | 0.00 | -81 |
| MLTX-02-005-EI | Material Submittal for Steel Tension Cables | 15 | 100% | 100% | 16-Apr-26 | 03-May-26 | 26-Aug-26 A | 26-Aug-26 A | 0.00 | 0.00 | 0.00 | -96 |
| MLTX-02-005-EI | Material Approval for Steel Tension Cables | 15 | 100% | 100% | 04-May-26 | 20-May-26 | 26-Aug-26 A | 26-Aug-26 A | 0.00 | 0.00 | 0.00 | -81 |
| **EMERGENCY DOORS** | | 28 | 0% | 0% | 16-Apr-26 | 20-May-26 | 26-Aug-26 A | 12-Sep-26 A | 0.00 | 0.00 | 0.00 | -95 |
| MLTX-02-005-EI | Material Submittal for Emergency Doors | 15 | 100% | 100% | 16-Apr-26 | 03-May-26 | 26-Aug-26 A | 26-Aug-26 A | 0.00 | 0.00 | 0.00 | -96 |
| MLTX-02-005-EI | Material Approval for Emergency Doors | 15 | 100% | 100% | 04-May-26 | 20-May-26 | 12-Sep-26 A | 12-Sep-26 A | 0.00 | 0.00 | 0.00 | -95 |
| **PRESSURE UNITS** | | 30 | 0% | 0% | 16-Apr-26 | 20-May-26 | 12-Sep-26 A | 12-Sep-26 A | 0.00 | 0.00 | 0.00 | -95 |
| MLTX-02-005-EI | Material Submittal for Pressure Units | 15 | 100% | 100% | 16-Apr-26 | 03-May-26 | 12-Sep-26 A | 12-Sep-26 A | 0.00 | 0.00 | 0.00 | -110 |
| MLTX-02-005-EI | Material Approval for Pressure Units | 15 | 100% | 100% | 04-May-26 | 20-May-26 | 12-Sep-26 A | 12-Sep-26 A | 0.00 | 0.00 | 0.00 | -95 |
| **AIR LOCK DOORS** | | 28 | 0% | 0% | 16-Apr-26 | 20-May-26 | 26-Aug-26 A | 12-Sep-26 A | 0.00 | 0.00 | 0.00 | -95 |
| MLTX-02-005-EI | Material Submittal for Lock Doors | 15 | 100% | 100% | 16-Apr-26 | 03-May-26 | 26-Aug-26 A | 26-Aug-26 A | 0.00 | 0.00 | 0.00 | -96 |
| MLTX-02-005-EI | Material Approval for Lock Doors | 15 | 100% | 100% | 04-May-26 | 20-May-26 | 12-Sep-26 A | 12-Sep-26 A | 0.00 | 0.00 | 0.00 | -95 |
| **ARTIFICIAL TURF** | | 30 | 0% | 0% | 16-Apr-26 | 20-May-26 | 19-Mar-26 A | 19-May-26 A | 0.00 | 0.00 | 0.00 | 1 |
| MLTX-02-005-EI | Material Submittal for Artificial TURF | 15 | 100% | 100% | 16-Apr-26 | 03-May-26 | 19-Mar-26 A | 14-May-26 A | 0.00 | 0.00 | 0.00 | -10 |
| MLTX-02-005-EI | Material Approval for Artificial TURF | 15 | 100% | 100% | 04-May-26 | 20-May-26 | 26-Mar-26 A | 19-May-26 A | 0.00 | 0.00 | 0.00 | 1 |
| **RUBBER GRANULES** | | 30 | 0% | 0% | 16-Apr-26 | 20-May-26 | 19-Mar-26 A | 19-May-26 A | 0.00 | 0.00 | 0.00 | 1 |
| MLTX-02-005-EI | Material Submittal for Rubber Granules | 15 | 100% | 100% | 16-Apr-26 | 03-May-26 | 19-Mar-26 A | 14-May-26 A | 0.00 | 0.00 | 0.00 | -10 |
| MLTX-02-005-EI | Material Approval for Rubber Granules | 15 | 100% | 100% | 04-May-26 | 20-May-26 | 26-Mar-26 A | 19-May-26 A | 0.00 | 0.00 | 0.00 | 1 |
| **PADEL GLASS** | | 30 | 0% | 0% | 16-Apr-26 | 20-May-26 | 19-Mar-26 A | 19-May-26 A | 0.00 | 0.00 | 0.00 | 1 |
| MLTX-02-005-EI | Material Submittal for Padel Glass | 15 | 100% | 100% | 16-Apr-26 | 03-May-26 | 19-Mar-26 A | 14-May-26 A | 0.00 | 0.00 | 0.00 | -10 |
| MLTX-02-005-EI | Material Approval for Padel Glass | 15 | 100% | 100% | 04-May-26 | 20-May-26 | 26-Mar-26 A | 19-May-26 A | 0.00 | 0.00 | 0.00 | 1 |
| **PADEL WIRE MESH/STEEL SETS** | | 30 | 0% | 0% | 16-Apr-26 | 20-May-26 | 19-Mar-26 A | 19-May-26 A | 0.00 | 0.00 | 0.00 | 1 |
| MLTX-02-005-EI | Material Submittal for Wire Mesh/Steel Sets | 15 | 100% | 100% | 16-Apr-26 | 03-May-26 | 19-Mar-26 A | 14-May-26 A | 0.00 | 0.00 | 0.00 | -10 |
| MLTX-02-005-EI | Material Approval for Wire Mesh/Steel Sets | 15 | 100% | 100% | 04-May-26 | 20-May-26 | 26-Mar-26 A | 19-May-26 A | 0.00 | 0.00 | 0.00 | 1 |
| **AGGREGATE BASE COURSE** | | 30 | 0% | 0% | 16-Apr-26 | 20-May-26 | 19-Mar-26 A | 10-May-26 A | 0.00 | 0.00 | 0.00 | 9 |
| MLTX-02-005-EI | Material Submittal for Aggregate Base Course | 15 | 100% | 100% | 16-Apr-26 | 03-May-26 | 19-Mar-26 A | 05-May-26 A | 0.00 | 0.00 | 0.00 | -2 |
| MLTX-02-005-EI | Material Approval for Aggregate Base Course | 15 | 100% | 100% | 04-May-26 | 20-May-26 | 26-Mar-26 A | 10-May-26 A | 0.00 | 0.00 | 0.00 | 9 |
| **BITUMINOUS BASE & WEARING COURSE** | | 30 | 0% | 0% | 04-May-26 | 10-Jun-26 | 24-Mar-26 A | 10-May-26 A | 0.00 | 0.00 | 0.00 | 24 |
| MLTX-02-005-EI | Material Submittal for Bituminous Base & Wearing Cource | 15 | 100% | 100% | 04-May-26 | 20-May-26 | 24-Mar-26 A | 05-May-26 A | 0.00 | 0.00 | 0.00 | 13 |
| MLTX-02-005-EI | Material Approval for the Site | 15 | 100% | 100% | 21-May-26 | 10-Jun-26 | 28-Mar-26 A | 10-May-26 A | 0.00 | 0.00 | 0.00 | 24 |
| **INTERLOCKING PAVING** | | 30 | 0% | 0% | 04-May-26 | 10-Jun-26 | 24-Mar-26 A | 13-May-26 A | 0.00 | 0.00 | 0.00 | 21 |
| MLTX-02-005-EI | Material Submittal for Interlocking Block Pavers | 15 | 100% | 100% | 04-May-26 | 20-May-26 | 24-Mar-26 A | 07-May-26 A | 0.00 | 0.00 | 0.00 | 11 |
| MLTX-02-005-EI | Material Approval for Interlocking Block Pavers | 15 | 100% | 100% | 21-May-26 | 10-Jun-26 | 28-Mar-26 A | 13-May-26 A | 0.00 | 0.00 | 0.00 | 21 |
| **MARKING PAINT** | | 30 | 0% | 0% | 04-May-26 | 10-Jun-26 | 24-Mar-26 A | 18-May-26 A | 0.00 | 0.00 | 0.00 | 17 |
| MLTX-02-005-EI | Material Submittal for Marking Paint | 15 | 100% | 100% | 04-May-26 | 20-May-26 | 24-Mar-26 A | 12-May-26 A | 0.00 | 0.00 | 0.00 | 7 |
| MLTX-02-005-EI | Material Approval for Marking Paint | 15 | 100% | 100% | 21-May-26 | 10-Jun-26 | 28-Mar-26 A | 18-May-26 A | 0.00 | 0.00 | 0.00 | 17 |
| **PACKAGE AC UNITS** | | 30 | 0% | 0% | 04-May-26 | 10-Jun-26 | 07-Jul-26 A | 07-Jul-26 A | 0.00 | 0.00 | 0.00 | -23 |
| MLTX-02-005-EI | Material Submittal for Package AC Units | 15 | 100% | 100% | 04-May-26 | 20-May-26 | 07-Jul-26 A | 07-Jul-26 A | 0.00 | 0.00 | 0.00 | -38 |
| MLTX-02-005-EI | Material Approval for Package AC Units | 15 | 100% | 100% | 21-May-26 | 10-Jun-26 | 07-Jul-26 A | 07-Jul-26 A | 0.00 | 0.00 | 0.00 | -23 |
| **AIR DIFUSSERS/GRILLS** | | 30 | 0% | 0% | 04-May-26 | 10-Jun-26 | 12-Sep-26 A | 12-Sep-26 A | 0.00 | 0.00 | 0.00 | -80 |
| MLTX-02-005-EI | Material Submittal for Air Difussers/Grills | 15 | 100% | 100% | 04-May-26 | 20-May-26 | 12-Sep-26 A | 12-Sep-26 A | 0.00 | 0.00 | 0.00 | -95 |
| MLTX-02-005-EI | Material Approval for Air Difussers/Grills | 15 | 100% | 100% | 21-May-26 | 10-Jun-26 | 12-Sep-26 A | 12-Sep-26 A | 0.00 | 0.00 | 0.00 | -80 |
| **GALVANIZED DUCTS** | | 30 | 0% | 0% | 04-May-26 | 10-Jun-26 | 24-Mar-26 A | 10-May-26 A | 0.00 | 0.00 | 0.00 | 24 |
| MLTX-02-005-EI | Material Submittal for Galvanized Duct | 15 | 100% | 100% | 04-May-26 | 20-May-26 | 24-Mar-26 A | 06-May-26 A | 0.00 | 0.00 | 0.00 | 12 |
| MLTX-02-005-EI | Material Approval for Galvanized Duct | 15 | 100% | 100% | 21-May-26 | 10-Jun-26 | 28-Mar-26 A | 10-May-26 A | 0.00 | 0.00 | 0.00 | 24 |
| **EXHAUST FANS** | | 30 | 0% | 0% | 04-May-26 | 10-Jun-26 | 12-Sep-26 A | 12-Sep-26 A | 0.00 | 0.00 | 0.00 | -80 |
| MLTX-02-005-EI | Material Submittal for Exhaust Fans | 15 | 100% | 100% | 04-May-26 | 20-May-26 | 12-Sep-26 A | 12-Sep-26 A | 0.00 | 0.00 | 0.00 | -95 |
| MLTX-02-005-EI | Material Approval for Exhaust Fans | 15 | 100% | 100% | 21-May-26 | 10-Jun-26 | 12-Sep-26 A | 12-Sep-26 A | 0.00 | 0.00 | 0.00 | -80 |
| **DISTRIBUTION BOARDS** | | 30 | 0% | 0% | 04-May-26 | 10-Jun-26 | 26-Aug-26 A | 26-Aug-26 A | 0.00 | 0.00 | 0.00 | -66 |
| MLTX-02-005-EI | Material Submittal for Distribution Boards | 15 | 100% | 100% | 04-May-26 | 20-May-26 | 26-Aug-26 A | 26-Aug-26 A | 0.00 | 0.00 | 0.00 | -81 |
| MLTX-02-005-EI | Material Approval for Distribution Boards | 15 | 100% | 100% | 21-May-26 | 10-Jun-26 | 26-Aug-26 A | 26-Aug-26 A | 0.00 | 0.00 | 0.00 | -66 |
| **POWER CABLES** | | 30 | 0% | 0% | 04-May-26 | 10-Jun-26 | 24-Mar-26 A | 19-May-26 A | 0.00 | 0.00 | 0.00 | 16 |
| MLTX-02-005-EI | Material Submittal for Power Cables | 15 | 100% | 100% | 04-May-26 | 20-May-26 | 24-Mar-26 A | 14-May-26 A | 0.00 | 0.00 | 0.00 | 5 |
| MLTX-02-005-EI | Material Approval for Power Cables | 15 | 100% | 100% | 21-May-26 | 10-Jun-26 | 28-Mar-26 A | 19-May-26 A | 0.00 | 0.00 | 0.00 | 16 |
| **LIGHT FIXTURES** | | 30 | 0% | 0% | 04-May-26 | 10-Jun-26 | 07-Jul-26 A | 07-Jul-26 A | 0.00 | 0.00 | 0.00 | -23 |
| MLTX-02-005-EI | Material Submittal for Light Fixtures | 15 | 100% | 100% | 04-May-26 | 20-May-26 | 07-Jul-26 A | 07-Jul-26 A | 0.00 | 0.00 | 0.00 | -38 |
| MLTX-02-005-EI | Material Approval for Light Fixtures | 15 | 100% | 100% | 21-May-26 | 10-Jun-26 | 07-Jul-26 A | 07-Jul-26 A | 0.00 | 0.00 | 0.00 | -23 |

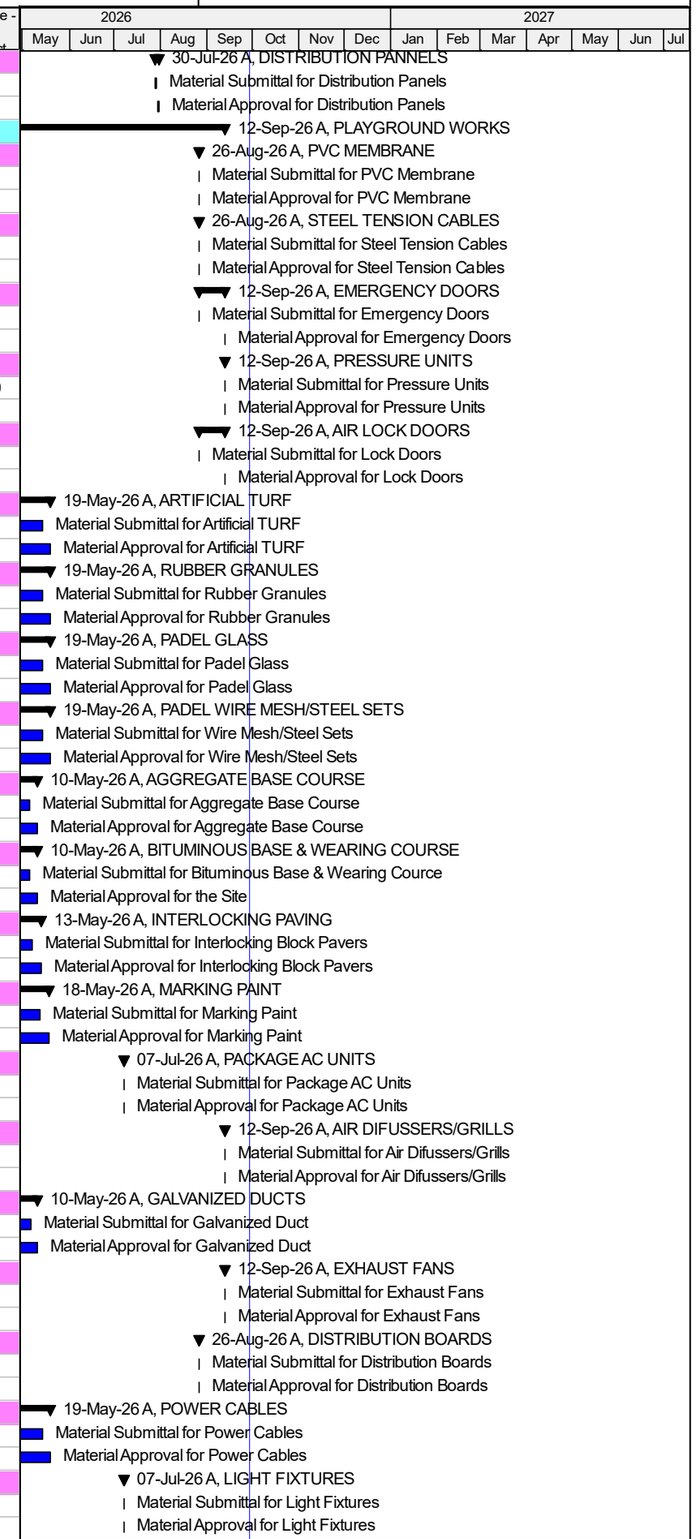


Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary




TASK filter: All Activities

© Oracle Corporation

# MLTX-02-005 - Playground Initiative for Eastern Region (Arar-Hasa osis -Dammam)

**Updateded schedule**
**D.D 28-09-2026**

| Activity ID | Activity Name | Original Duration | Schedule % Complete | Performance % Complete | BL Project Start | BL Project Finish | Start | Finish | Planned Value Cost | Earned Value Cost | Budgeted Total Cost | Variance - BL Project |
|---|---|---|---|---|---|---|---|---|---|---|---|---|
| **CCTV MATERIALS** | | 28 | 0% | 0% | 04-May-26 | 10-Jun-26 | 26-Aug-26 A | 12-Sep-26 A | 0.00 | 0.00 | 0.00 | -80 |
| MLTX-02-005-EM | Material Submittal for CCTV | 15 | 100% | 100% | 04-May-26 | 20-May-26 | 26-Aug-26 A | 26-Aug-26 A | 0.00 | 0.00 | 0.00 | -81 |
| MLTX-02-005-EM | Material Approval for CCTV | 15 | 100% | 100% | 21-May-26 | 10-Jun-26 | 12-Sep-26 A | 12-Sep-26 A | 0.00 | 0.00 | 0.00 | -80 |
| **POWER OUTLETS/SWITCHES** | | 30 | 0% | 0% | 04-May-26 | 10-Jun-26 | 12-Sep-26 A | 12-Sep-26 A | 0.00 | 0.00 | 0.00 | -80 |
| MLTX-02-005-EM | Material Submittal for Power Outlets/Switches | 15 | 100% | 100% | 04-May-26 | 20-May-26 | 12-Sep-26 A | 12-Sep-26 A | 0.00 | 0.00 | 0.00 | -95 |
| MLTX-02-005-EM | Material Approval for Power Outlets/Switches | 15 | 100% | 100% | 21-May-26 | 10-Jun-26 | 12-Sep-26 A | 12-Sep-26 A | 0.00 | 0.00 | 0.00 | -80 |
| **LANDSCAPE WORKS** | | 66 | 0% | 0% | 04-May-26 | 10-Jun-26 | 24-Mar-26 A | 30-Jul-26 A | 0.00 | 0.00 | 0.00 | -43 |
| **INTERLOCKING PAVING** | | 30 | 0% | 0% | 04-May-26 | 10-Jun-26 | 24-Mar-26 A | 13-May-26 A | 0.00 | 0.00 | 0.00 | 21 |
| MLTX-02-005-EM | Material Submittal for Interlocking Block Pavers | 15 | 100% | 100% | 04-May-26 | 20-May-26 | 24-Mar-26 A | 07-May-26 A | 0.00 | 0.00 | 0.00 | 11 |
| MLTX-02-005-EM | Material Approval for Interlocking Block Pavers | 15 | 100% | 100% | 21-May-26 | 10-Jun-26 | 28-Mar-26 A | 13-May-26 A | 0.00 | 0.00 | 0.00 | 21 |
| **CURBSTONE** | | 30 | 0% | 0% | 04-May-26 | 10-Jun-26 | 24-Mar-26 A | 13-May-26 A | 0.00 | 0.00 | 0.00 | 21 |
| MLTX-02-005-EM | Material Submittal for Curbstone | 15 | 100% | 100% | 04-May-26 | 20-May-26 | 24-Mar-26 A | 07-May-26 A | 0.00 | 0.00 | 0.00 | 11 |
| MLTX-02-005-EM | Material Approval for Curbstone | 15 | 100% | 100% | 21-May-26 | 10-Jun-26 | 28-Mar-26 A | 13-May-26 A | 0.00 | 0.00 | 0.00 | 21 |
| **PAVEMENT MARKING** | | 30 | 0% | 0% | 04-May-26 | 10-Jun-26 | 24-Mar-26 A | 18-May-26 A | 0.00 | 0.00 | 0.00 | 17 |
| MLTX-02-005-EM | Material Submittal for Pavement Markings | 15 | 100% | 100% | 04-May-26 | 20-May-26 | 24-Mar-26 A | 12-May-26 A | 0.00 | 0.00 | 0.00 | 7 |
| MLTX-02-005-EM | Material Approval for Pavement Markings | 15 | 100% | 100% | 21-May-26 | 10-Jun-26 | 28-Mar-26 A | 18-May-26 A | 0.00 | 0.00 | 0.00 | 17 |
| **TRAFFIC SIGNS** | | 30 | 0% | 0% | 04-May-26 | 10-Jun-26 | 24-Mar-26 A | 18-May-26 A | 0.00 | 0.00 | 0.00 | 17 |
| MLTX-02-005-EM | Material Submittal for Traffic Signs | 15 | 100% | 100% | 04-May-26 | 20-May-26 | 24-Mar-26 A | 12-May-26 A | 0.00 | 0.00 | 0.00 | 7 |
| MLTX-02-005-EM | Material Approval for Traffic Signs | 15 | 100% | 100% | 21-May-26 | 10-Jun-26 | 28-Mar-26 A | 18-May-26 A | 0.00 | 0.00 | 0.00 | 17 |
| **IRRIGATION PIPES/SPRINKLERS** | | 30 | 0% | 0% | 04-May-26 | 10-Jun-26 | 28-Jul-26 A | 30-Jul-26 A | 0.00 | 0.00 | 0.00 | -43 |
| MLTX-02-005-EM | Material Submittal for Irrigation Pipes/Sprinkles | 15 | 100% | 100% | 04-May-26 | 20-May-26 | 28-Jul-26 A | 28-Jul-26 A | 0.00 | 0.00 | 0.00 | -56 |
| MLTX-02-005-EM | Material Approval for Irrigation Pipes/Sprinkles | 15 | 100% | 100% | 21-May-26 | 10-Jun-26 | 30-Jul-26 A | 30-Jul-26 A | 0.00 | 0.00 | 0.00 | -43 |
| **AGRICULTURE SOIL** | | 30 | 0% | 0% | 04-May-26 | 10-Jun-26 | 24-Mar-26 A | 21-May-26 A | 0.00 | 0.00 | 0.00 | 14 |
| MLTX-02-005-EM | Material Submittal for Agriculture Soil | 15 | 100% | 100% | 04-May-26 | 20-May-26 | 24-Mar-26 A | 16-May-26 A | 0.00 | 0.00 | 0.00 | 4 |
| MLTX-02-005-EM | Material Approval for Agriculture Soil | 15 | 100% | 100% | 21-May-26 | 10-Jun-26 | 28-Mar-26 A | 21-May-26 A | 0.00 | 0.00 | 0.00 | 14 |
| **TRACK SURFACE** | | 30 | 0% | 0% | 04-May-26 | 10-Jun-26 | 28-Jul-26 A | 30-Jul-26 A | 0.00 | 0.00 | 0.00 | -43 |
| MLTX-02-005-EM | Material Submittal for Track Surface | 15 | 100% | 100% | 04-May-26 | 20-May-26 | 28-Jul-26 A | 28-Jul-26 A | 0.00 | 0.00 | 0.00 | -56 |
| MLTX-02-005-EM | Material Approval for Track Surface | 15 | 100% | 100% | 21-May-26 | 10-Jun-26 | 30-Jul-26 A | 30-Jul-26 A | 0.00 | 0.00 | 0.00 | -43 |
| **GRASS/TREES** | | 30 | 0% | 0% | 04-May-26 | 10-Jun-26 | 24-Mar-26 A | 21-May-26 A | 0.00 | 0.00 | 0.00 | 14 |
| MLTX-02-005-EM | Material Submittal for Grass/Trees | 15 | 100% | 100% | 04-May-26 | 20-May-26 | 24-Mar-26 A | 16-May-26 A | 0.00 | 0.00 | 0.00 | 4 |
| MLTX-02-005-EM | Material Approval for Grass/Trees | 15 | 100% | 100% | 21-May-26 | 10-Jun-26 | 28-Mar-26 A | 21-May-26 A | 0.00 | 0.00 | 0.00 | 14 |
| **CABLES** | | 30 | 0% | 0% | 04-May-26 | 10-Jun-26 | 24-Mar-26 A | 19-May-26 A | 0.00 | 0.00 | 0.00 | 16 |
| MLTX-02-005-EM | Material Submittal for Cables | 15 | 100% | 100% | 04-May-26 | 20-May-26 | 24-Mar-26 A | 14-May-26 A | 0.00 | 0.00 | 0.00 | 5 |
| MLTX-02-005-EM | Material Approval for Cables | 15 | 100% | 100% | 21-May-26 | 10-Jun-26 | 28-Mar-26 A | 19-May-26 A | 0.00 | 0.00 | 0.00 | 16 |
| **LIGHT POLES** | | 30 | 0% | 0% | 04-May-26 | 10-Jun-26 | 07-Jul-26 A | 07-Jul-26 A | 0.00 | 0.00 | 0.00 | -23 |
| MLTX-02-005-EM | Material Submittal for Lighting poles | 15 | 100% | 100% | 04-May-26 | 20-May-26 | 07-Jul-26 A | 07-Jul-26 A | 0.00 | 0.00 | 0.00 | -38 |
| MLTX-02-005-EM | Material Approval for Lighting poles | 15 | 100% | 100% | 21-May-26 | 10-Jun-26 | 07-Jul-26 A | 07-Jul-26 A | 0.00 | 0.00 | 0.00 | -23 |
| **PROCUREMENT** | | 183 | 0% | 0% | 21-May-26 | 08-Nov-26 | 04-Apr-26 A | 13-Feb-27 | 0.00 | 0.00 | 0.00 | -83 |
| **SHORT LEAD ITEM** | | 183 | 0% | 0% | 21-May-26 | 21-Oct-26 | 04-Apr-26 A | 13-Feb-27 | 0.00 | 0.00 | 0.00 | -98 |
| **TOILET/SERVICE WORKS** | | 94 | 0% | 0% | 21-May-26 | 11-Aug-26 | 04-Apr-26 A | 01-Nov-26 | 0.00 | 0.00 | 0.00 | -69 |
| **STEEL REINFORCEMENT** | | 10 | 0% | 0% | 21-May-26 | 04-Jun-26 | 04-Apr-26 A | 19-May-26 A | 0.00 | 0.00 | 0.00 | 11 |
| MLTX-02-005-PR-1 | PO for Steel Reinforcement | 5 | 100% | 100% | 21-May-26 | 30-May-26 | 04-Apr-26 A | 18-May-26 A | 0.00 | 0.00 | 0.00 | 7 |
| MLTX-02-005-PR-1 | Material Delivery of Steel Reinforcement | 5 | 100% | 100% | 31-May-26 | 04-Jun-26 | 09-Apr-26 A | 19-May-26 A | 0.00 | 0.00 | 0.00 | 11 |
| **CONCRETE BLOCKS** | | 61 | 0% | 0% | 31-May-26 | 14-Jun-26 | 09-Apr-26 A | 07-Jul-26 A | 0.00 | 0.00 | 0.00 | -20 |
| MLTX-02-005-PR-1 | PO for Concrete Blocks | 5 | 100% | 100% | 31-May-26 | 04-Jun-26 | 09-Apr-26 A | 18-May-26 A | 0.00 | 0.00 | 0.00 | 12 |
| MLTX-02-005-PR-1 | Material Delivery of Concrete Blocks | 8 | 100% | 100% | 06-Jun-26 | 14-Jun-26 | 07-Jul-26 A | 07-Jul-26 A | 0.00 | 0.00 | 0.00 | -20 |
| **FLOOR/WALL TILES** | | 18 | 0% | 0% | 06-Jun-26 | 25-Jun-26 | 18-Aug-26 A | 18-Aug-26 A | 0.00 | 0.00 | 0.00 | -46 |
| MLTX-02-005-PR-1 | PO for Tilling Materials | 5 | 100% | 100% | 06-Jun-26 | 10-Jun-26 | 18-Aug-26 A | 18-Aug-26 A | 0.00 | 0.00 | 0.00 | -59 |
| MLTX-02-005-PR-1 | Material Delivery of Tailling Material | 13 | 100% | 100% | 11-Jun-26 | 25-Jun-26 | 18-Aug-26 A | 18-Aug-26 A | 0.00 | 0.00 | 0.00 | -46 |
| **SUSPENDED CEILING** | | 18 | 0% | 0% | 22-Jul-26 | 11-Aug-26 | 18-Aug-26 A | 18-Aug-26 A | 0.00 | 0.00 | 0.00 | -6 |
| MLTX-02-005-PR-1 | PO for Suspend Ceiling | 5 | 100% | 100% | 22-Jul-26 | 27-Jul-26 | 18-Aug-26 A | 18-Aug-26 A | 0.00 | 0.00 | 0.00 | -19 |
| MLTX-02-005-PR-1 | Material Delivery of Suspend Ceiling | 13 | 100% | 100% | 28-Jul-26 | 11-Aug-26 | 18-Aug-26 A | 18-Aug-26 A | 0.00 | 0.00 | 0.00 | -6 |
| **DOORS/WINDOWS** | | 20 | 0% | 0% | 11-Jun-26 | 04-Jul-26 | 15-Sep-26 A | 15-Sep-26 A | 0.00 | 0.00 | 0.00 | -63 |
| MLTX-02-005-PR-1 | PO for Doors/Windows | 5 | 100% | 100% | 11-Jun-26 | 16-Jun-26 | 15-Sep-26 A | 15-Sep-26 A | 0.00 | 0.00 | 0.00 | -78 |
| MLTX-02-005-PR-1 | Material Delivery for Doors/Windows | 15 | 100% | 100% | 17-Jun-26 | 04-Jul-26 | 15-Sep-26 A | 15-Sep-26 A | 0.00 | 0.00 | 0.00 | -63 |
| **WATER SUPPLY PIPES** | | 12 | 0% | 0% | 17-Jun-26 | 30-Jun-26 | 07-Jul-26 A | 07-Jul-26 A | 0.00 | 0.00 | 0.00 | -6 |
| MLTX-02-005-PR-1 | PO for Water Supply Pipes | 5 | 100% | 100% | 17-Jun-26 | 22-Jun-26 | 07-Jul-26 A | 07-Jul-26 A | 0.00 | 0.00 | 0.00 | -13 |
| MLTX-02-005-PR-1 | Material Delivery for Water Supply Pipes | 7 | 100% | 100% | 23-Jun-26 | 30-Jun-26 | 07-Jul-26 A | 07-Jul-26 A | 0.00 | 0.00 | 0.00 | -6 |
| **SEWAGE/DRAINAGE PIPES** | | 12 | 0% | 0% | 17-Jun-26 | 30-Jun-26 | 02-Jun-26 A | 10-Jun-26 A | 0.00 | 0.00 | 0.00 | 17 |
| MLTX-02-005-PR-1 | PO for Sewage/Drainage Pipes | 5 | 100% | 100% | 17-Jun-26 | 22-Jun-26 | 02-Jun-26 A | 02-Jun-26 A | 0.00 | 0.00 | 0.00 | 17 |
| MLTX-02-005-PR-1 | Material Delivery for Sewage/Drainage Pipes | 7 | 100% | 100% | 23-Jun-26 | 30-Jun-26 | 10-Jun-26 A | 10-Jun-26 A | 0.00 | 0.00 | 0.00 | 17 |
| **SANITARY FIXTURES** | | 18 | 0% | 0% | 23-Jun-26 | 13-Jul-26 | 18-Aug-26 A | 18-Aug-26 A | 0.00 | 0.00 | 0.00 | -31 |
| MLTX-02-005-PR-1 | PO for Sanitary Fixtures | 5 | 100% | 100% | 23-Jun-26 | 28-Jun-26 | 18-Aug-26 A | 18-Aug-26 A | 0.00 | 0.00 | 0.00 | -44 |
| MLTX-02-005-PR-1 | Material Delivery for Sanitary Fixtures | 13 | 100% | 100% | 29-Jun-26 | 13-Jul-26 | 18-Aug-26 A | 18-Aug-26 A | 0.00 | 0.00 | 0.00 | -31 |

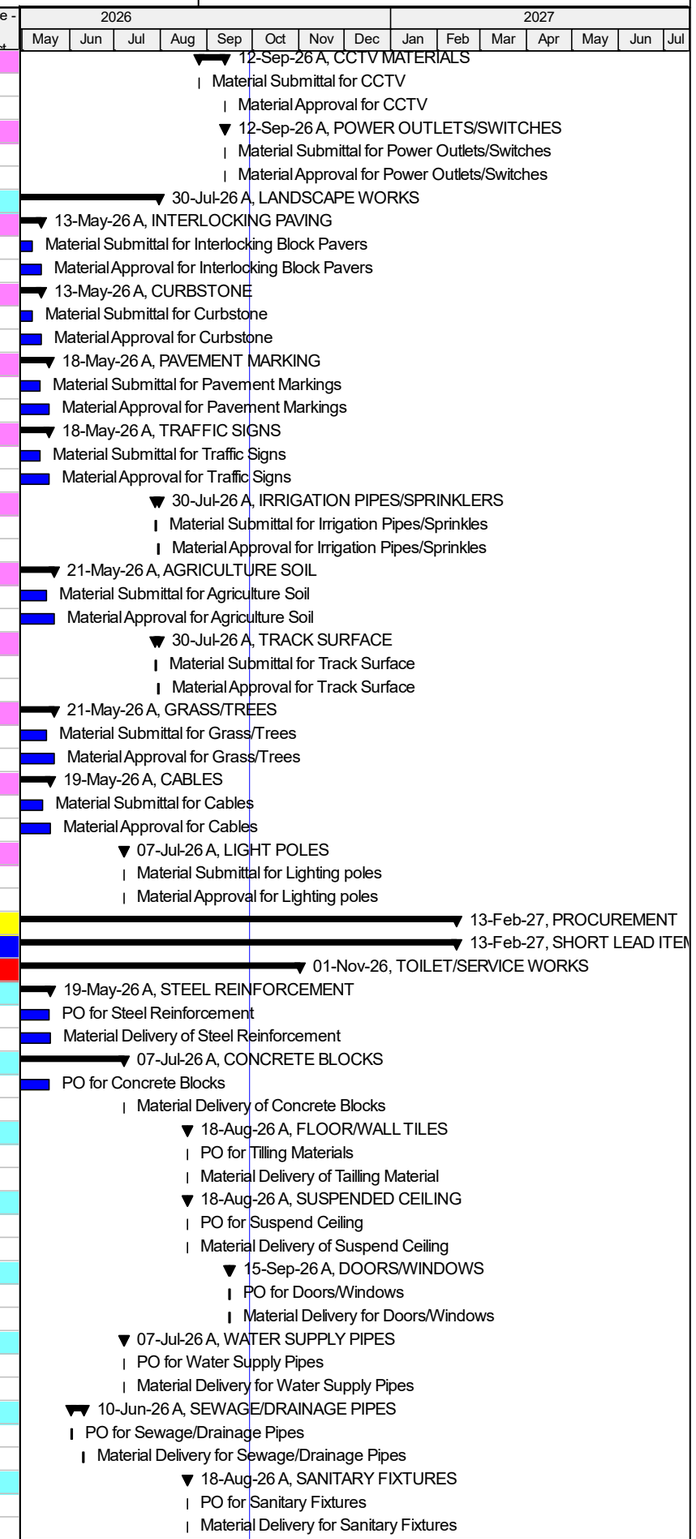


Actual Level of Effort | Actual Work | Remaining Work | Critical Remaining Work | Milestone | summary




TASK filter: All Activities

© Oracle Corporation

# MLTX-02-005 - Playground Initiative for Eastern Region (Arar-Hasa osis -Dammam)

**Updateded schedule**
**D.D 28-09-2026**

| Activity ID | Activity Name | Original Duration | Schedule % Complete | Performance % Complete | BL Project Start | BL Project Finish | Start | Finish | Planned Value Cost | Earned Value Cost | Budgeted Total Cost | Variance - BL Project |
|---|---|---|---|---|---|---|---|---|---|---|---|---|
| **PACKAGE AC UNITS** | | 20 | 0% | 0% | 29-Jun-26 | 21-Jul-26 | 07-Jul-26 A | 07-Jul-26 A | 0.00 | 0.00 | 0.00 | 12 |
| MLTX-02-005-PR-1 | PO for Package AC Units | 5 | 100% | 100% | 29-Jun-26 | 04-Jul-26 | 07-Jul-26 A | 07-Jul-26 A | 0.00 | 0.00 | 0.00 | -3 |
| MLTX-02-005-PR-1 | Material Delivery for Package AC Units | 15 | 100% | 100% | 05-Jul-26 | 21-Jul-26 | 07-Jul-26 A | 07-Jul-26 A | 0.00 | 0.00 | 0.00 | 12 |
| **AIR DIFUSSERS/GRILLS** | | 20 | 0% | 0% | 29-Jun-26 | 21-Jul-26 | 18-Aug-26 A | 18-Aug-26 A | 0.00 | 0.00 | 0.00 | -24 |
| MLTX-02-005-PR-1 | PO for Air Diffusers/Grills | 5 | 100% | 100% | 29-Jun-26 | 04-Jul-26 | 18-Aug-26 A | 18-Aug-26 A | 0.00 | 0.00 | 0.00 | -39 |
| MLTX-02-005-PR-1 | Material Delivery for Air Diffusers/Grills | 15 | 100% | 100% | 05-Jul-26 | 21-Jul-26 | 18-Aug-26 A | 18-Aug-26 A | 0.00 | 0.00 | 0.00 | -24 |
| **GALVANIZED DUCTS** | | 20 | 0% | 0% | 29-Jun-26 | 21-Jul-26 | 18-Aug-26 A | 18-Aug-26 A | 0.00 | 0.00 | 0.00 | -24 |
| MLTX-02-005-PR-1 | PO for Galvanized Ducts | 5 | 100% | 100% | 29-Jun-26 | 04-Jul-26 | 18-Aug-26 A | 18-Aug-26 A | 0.00 | 0.00 | 0.00 | -39 |
| MLTX-02-005-PR-1 | Material Delivery for Galvanized Ducts | 15 | 100% | 100% | 05-Jul-26 | 21-Jul-26 | 18-Aug-26 A | 18-Aug-26 A | 0.00 | 0.00 | 0.00 | -24 |
| **EXHAUST FANS** | | 15 | 0% | 0% | 29-Jun-26 | 15-Jul-26 | 18-Aug-26 A | 18-Aug-26 A | 0.00 | 0.00 | 0.00 | -29 |
| MLTX-02-005-PR-1 | PO for Exhaust Fans | 5 | 100% | 100% | 29-Jun-26 | 04-Jul-26 | 18-Aug-26 A | 18-Aug-26 A | 0.00 | 0.00 | 0.00 | -39 |
| MLTX-02-005-PR-1 | Material Delivery for Exhaust Fans | 10 | 100% | 100% | 05-Jul-26 | 15-Jul-26 | 18-Aug-26 A | 18-Aug-26 A | 0.00 | 0.00 | 0.00 | -29 |
| **LIGHTING FIXTURES** | | 25 | 0% | 0% | 05-Jul-26 | 21-Jul-26 | 07-Jul-26 A | 10-Oct-26 | 0.00 | 0.00 | 0.00 | -68 |
| MLTX-02-005-PR-1 | PO for Lighting Fixtures | 5 | 100% | 100% | 05-Jul-26 | 09-Jul-26 | 07-Jul-26 A | 07-Jul-26 A | 0.00 | 0.00 | 0.00 | 2 |
| MLTX-02-005-PR-1 | Material Delivery for Lighting Fixtures | 10 | 100% | 0% | 11-Jul-26 | 21-Jul-26 | 29-Sep-26 | 10-Oct-26 | 0.00 | 0.00 | 0.00 | -68 |
| **SWITCHES/SOCKETS** | | 12 | 0% | 0% | 11-Jul-26 | 23-Jul-26 | 29-Sep-26 | 12-Oct-26 | 0.00 | 0.00 | 0.00 | -68 |
| MLTX-02-005-PR-1 | PO for Switches/Sockets | 5 | 100% | 0% | 11-Jul-26 | 15-Jul-26 | 29-Sep-26 | 04-Oct-26 | 0.00 | 0.00 | 0.00 | -68 |
| MLTX-02-005-PR-1 | Material Delivery for Switches/Sockets | 7 | 100% | 0% | 16-Jul-26 | 23-Jul-26 | 05-Oct-26 | 12-Oct-26 | 0.00 | 0.00 | 0.00 | -68 |
| **EARTHING SYSTEM** | | 27 | 0% | 0% | 11-Jun-26 | 12-Jul-26 | 12-Jul-26 A | 12-Jul-26 A | 0.00 | 0.00 | 0.00 | 0 |
| MLTX-02-005-PR-1 | PO for Earthing System | 5 | 100% | 100% | 11-Jun-26 | 16-Jun-26 | 12-Jul-26 A | 12-Jul-26 A | 0.00 | 0.00 | 0.00 | -22 |
| MLTX-02-005-PR-1 | Material Delivery for Earthing System | 15 | 100% | 100% | 25-Jun-26 | 12-Jul-26 | 12-Jul-26 A | 12-Jul-26 A | 0.00 | 0.00 | 0.00 | 0 |
| **DISTRIBUTION PANNELS** | | 20 | 0% | 0% | 11-Jun-26 | 04-Jul-26 | 29-Sep-26 | 21-Oct-26 | 0.00 | 0.00 | 0.00 | -93 |
| MLTX-02-005-PR-1 | PO for Distribution Panels | 5 | 100% | 0% | 11-Jun-26 | 16-Jun-26 | 29-Sep-26 | 04-Oct-26 | 0.00 | 0.00 | 0.00 | -93 |
| MLTX-02-005-PR-1 | Material Delivery for Distribution Panels | 15 | 100% | 0% | 17-Jun-26 | 04-Jul-26 | 05-Oct-26 | 21-Oct-26 | 0.00 | 0.00 | 0.00 | -93 |
| **FURNITURES** | | 29 | 0% | 0% | 05-Jul-26 | 06-Aug-26 | 29-Sep-26 | 01-Nov-26 | 0.00 | 0.00 | 0.00 | -73 |
| MLTX-02-005-PR-1 | PO for Furnitures | 9 | 100% | 0% | 05-Jul-26 | 14-Jul-26 | 29-Sep-26 | 08-Oct-26 | 0.00 | 0.00 | 0.00 | -73 |
| MLTX-02-005-PR-1 | Material Delivery for Furnitures | 20 | 100% | 0% | 15-Jul-26 | 06-Aug-26 | 10-Oct-26 | 01-Nov-26 | 0.00 | 0.00 | 0.00 | -73 |
| **PLAYGROUND WORKS** | | 115 | 0% | 0% | 21-May-26 | 29-Aug-26 | 04-Apr-26 A | 25-Nov-26 | 0.00 | 0.00 | 0.00 | -75 |
| **PVC MEMBRANE** | | 35 | 0% | 0% | 21-May-26 | 29-Jun-26 | 04-Apr-26 A | 22-Oct-26 | 0.00 | 0.00 | 0.00 | -98 |
| MLTX-02-005-PR-1 | PO for PVC Membrane | 10 | 100% | 100% | 21-May-26 | 04-Jun-26 | 04-Apr-26 A | 19-May-26 A | 0.00 | 0.00 | 0.00 | 11 |
| MLTX-02-005-PR-1 | Material Delivery for PVC Membrane | 21 | 100% | 0% | 06-Jun-26 | 29-Jun-26 | 29-Sep-26 | 22-Oct-26 | 0.00 | 0.00 | 0.00 | -98 |
| **ARTIFICIAL TURF** | | 16 | 0% | 0% | 30-Jun-26 | 19-Jul-26 | 04-Apr-26 A | 05-Nov-26 | 0.00 | 0.00 | 0.00 | -93 |
| MLTX-02-005-PR-1 | PO for Artificial TURF | 5 | 100% | 100% | 30-Jun-26 | 05-Jul-26 | 04-Apr-26 A | 19-May-26 A | 0.00 | 0.00 | 0.00 | 37 |
| MLTX-02-005-PR-1 | Material Delivery for Artificial TURF | 12 | 100% | 0% | 06-Jul-26 | 19-Jul-26 | 24-Oct-26 | 05-Nov-26 | 0.00 | 0.00 | 0.00 | -93 |
| **RUBBER GRANULES** | | 26 | 0% | 0% | 21-May-26 | 13-Jun-26 | 04-Apr-26 A | 12-Oct-26 | 0.00 | 0.00 | 0.00 | -103 |
| MLTX-02-005-PR-1 | PO for Rubber Granules | 5 | 100% | 100% | 21-May-26 | 30-May-26 | 04-Apr-26 A | 19-May-26 A | 0.00 | 0.00 | 0.00 | 6 |
| MLTX-02-005-PR-1 | Material Delivery for Rubber Granules | 12 | 100% | 0% | 31-May-26 | 13-Jun-26 | 29-Sep-26 | 12-Oct-26 | 0.00 | 0.00 | 0.00 | -103 |
| **PADEL GLASS** | | 32 | 0% | 0% | 21-May-26 | 20-Jun-26 | 04-Apr-26 A | 19-Oct-26 | 0.00 | 0.00 | 0.00 | -103 |
| MLTX-02-005-PR-1 | PO for Padel Glass | 5 | 100% | 100% | 21-May-26 | 30-May-26 | 04-Apr-26 A | 19-May-26 A | 0.00 | 0.00 | 0.00 | 6 |
| MLTX-02-005-PR-1 | Material Delivery for Padel Glass | 18 | 100% | 0% | 31-May-26 | 20-Jun-26 | 29-Sep-26 | 19-Oct-26 | 0.00 | 0.00 | 0.00 | -103 |
| **PADEL WIRE MESH/STEEL SETS** | | 24 | 0% | 0% | 31-May-26 | 22-Jun-26 | 09-Apr-26 A | 15-Oct-26 | 0.00 | 0.00 | 0.00 | -98 |
| MLTX-02-005-PR-1 | PO for Wire Mesh/Steel Sets | 5 | 100% | 100% | 31-May-26 | 04-Jun-26 | 09-Apr-26 A | 19-May-26 A | 0.00 | 0.00 | 0.00 | 11 |
| MLTX-02-005-PR-1 | Material Delivery for Wire Mesh/Steel Sets | 15 | 100% | 0% | 06-Jun-26 | 22-Jun-26 | 29-Sep-26 | 15-Oct-26 | 0.00 | 0.00 | 0.00 | -98 |
| **AGGREGATE BASE COURSE** | | 56 | 0% | 0% | 21-May-26 | 07-Jun-26 | 04-Apr-26 A | 07-Jul-26 A | 0.00 | 0.00 | 0.00 | -26 |
| MLTX-02-005-PR-1 | PO for Aggregate Base Course | 5 | 100% | 100% | 21-May-26 | 30-May-26 | 04-Apr-26 A | 14-May-26 A | 0.00 | 0.00 | 0.00 | 10 |
| MLTX-02-005-PR-1 | Material Delivery for Aggregate Base Course | 7 | 100% | 100% | 31-May-26 | 07-Jun-26 | 07-Jul-26 A | 07-Jul-26 A | 0.00 | 0.00 | 0.00 | -26 |
| **BITUMINOUS BASE & WEARING COURSE** | | 12 | 0% | 0% | 11-Jun-26 | 24-Jun-26 | 29-Sep-26 | 12-Oct-26 | 0.00 | 0.00 | 0.00 | -93 |
| MLTX-02-005-PR-1 | PO for Bituminous Base & Wearing Course | 5 | 100% | 0% | 11-Jun-26 | 16-Jun-26 | 29-Sep-26 | 04-Oct-26 | 0.00 | 0.00 | 0.00 | -93 |
| MLTX-02-005-PR-1 | Material Delivery for the Site | 7 | 100% | 0% | 17-Jun-26 | 24-Jun-26 | 05-Oct-26 | 12-Oct-26 | 0.00 | 0.00 | 0.00 | -93 |
| **INTERLOCKING PAVING** | | 12 | 0% | 0% | 16-Jul-26 | 29-Jul-26 | 19-Oct-26 | 01-Nov-26 | 0.00 | 0.00 | 0.00 | -80 |
| MLTX-02-005-PR-1 | PO for Interlocking Block Pavers | 5 | 100% | 0% | 16-Jul-26 | 21-Jul-26 | 19-Oct-26 | 24-Oct-26 | 0.00 | 0.00 | 0.00 | -80 |
| MLTX-02-005-PR-1 | Material Delivery for Interlocking Block Pavers | 7 | 100% | 0% | 22-Jul-26 | 29-Jul-26 | 25-Oct-26 | 01-Nov-26 | 0.00 | 0.00 | 0.00 | -80 |
| **MARKING PAINT** | | 12 | 0% | 0% | 17-Jun-26 | 30-Jun-26 | 05-Oct-26 | 18-Oct-26 | 0.00 | 0.00 | 0.00 | -93 |
| MLTX-02-005-PR-1 | PO for Marking Paint | 5 | 100% | 0% | 17-Jun-26 | 22-Jun-26 | 05-Oct-26 | 10-Oct-26 | 0.00 | 0.00 | 0.00 | -93 |
| MLTX-02-005-PR-1 | Material Delivery for Marking Paint | 7 | 100% | 0% | 23-Jun-26 | 30-Jun-26 | 11-Oct-26 | 18-Oct-26 | 0.00 | 0.00 | 0.00 | -93 |
| **PACKAGE AC UNITS** | | 20 | 0% | 0% | 20-Jul-26 | 11-Aug-26 | 07-Jul-26 A | 07-Jul-26 A | 0.00 | 0.00 | 0.00 | 30 |
| MLTX-02-005-PR-1 | PO for Package AC Units | 5 | 100% | 100% | 20-Jul-26 | 25-Jul-26 | 07-Jul-26 A | 07-Jul-26 A | 0.00 | 0.00 | 0.00 | 15 |
| MLTX-02-005-PR-1 | Material Delivery for Package AC Units | 15 | 100% | 100% | 26-Jul-26 | 11-Aug-26 | 07-Jul-26 A | 07-Jul-26 A | 0.00 | 0.00 | 0.00 | 30 |
| **AIR DIFUSSERS/GRILLS** | | 20 | 0% | 0% | 05-Jul-26 | 27-Jul-26 | 29-Sep-26 | 21-Oct-26 | 0.00 | 0.00 | 0.00 | -73 |
| MLTX-02-005-PR-1 | PO for Air Difussers/Grills | 5 | 100% | 0% | 05-Jul-26 | 09-Jul-26 | 29-Sep-26 | 04-Oct-26 | 0.00 | 0.00 | 0.00 | -73 |
| MLTX-02-005-PR-1 | Material Delivery for Air Difussers/Grills | 15 | 100% | 0% | 11-Jul-26 | 27-Jul-26 | 05-Oct-26 | 21-Oct-26 | 0.00 | 0.00 | 0.00 | -73 |
| **GALVANIZED DUCTS** | | 20 | 0% | 0% | 05-Jul-26 | 27-Jul-26 | 29-Sep-26 | 21-Oct-26 | 0.00 | 0.00 | 0.00 | -73 |
| MLTX-02-005-PR-1 | PO for Galvanized Duct | 5 | 100% | 0% | 05-Jul-26 | 09-Jul-26 | 29-Sep-26 | 04-Oct-26 | 0.00 | 0.00 | 0.00 | -73 |
| MLTX-02-005-PR-1 | Material Delivery for Galvanized Duct | 15 | 100% | 0% | 11-Jul-26 | 27-Jul-26 | 05-Oct-26 | 21-Oct-26 | 0.00 | 0.00 | 0.00 | -73 |

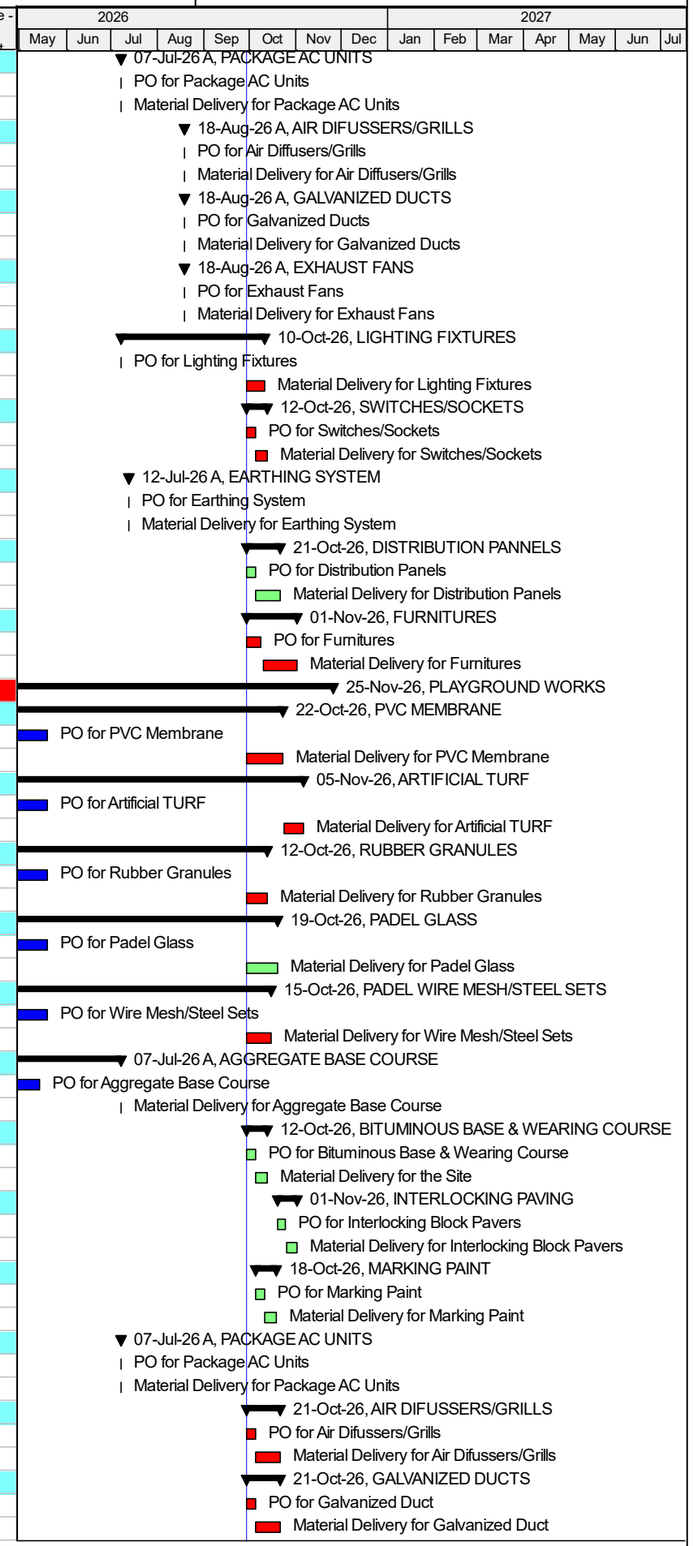


Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary




TASK filter: All Activities

© Oracle Corporation

# MLTX-02-005 - Playground Initiative for Eastern Region (Arar-Hasa osis -Dammam)

**Updateded schedule**
**D.D 28-09-2026**

| Activity ID | Activity Name | Original Duration | Schedule % Complete | Performance % Complete | BL Project Start | BL Project Finish | Start | Finish | Planned Value Cost | Earned Value Cost | Budgeted Total Cost | Variance - BL Project |
|---|---|---|---|---|---|---|---|---|---|---|---|---|
| **EXHAUST FANS** | | 20 | 0% | 0% | 05-Jul-26 | 27-Jul-26 | 29-Sep-26 | 21-Oct-26 | 0.00 | 0.00 | 0.00 | -73 |
| MLTX-02-005-PR-1 | PO for Exhaust Fans | 5 | 100% | 0% | 05-Jul-26 | 09-Jul-26 | 29-Sep-26 | 04-Oct-26 | 0.00 | 0.00 | 0.00 | -73 |
| MLTX-02-005-PR-1 | Material Delivery for Exhaust Fans | 15 | 100% | 0% | 11-Jul-26 | 27-Jul-26 | 05-Oct-26 | 21-Oct-26 | 0.00 | 0.00 | 0.00 | -73 |
| **DISTRIBUTION BOARDS** | | 20 | 0% | 0% | 05-Jul-26 | 27-Jul-26 | 17-Oct-26 | 08-Nov-26 | 0.00 | 0.00 | 0.00 | -88 |
| MLTX-02-005-PR-1 | PO for Distribution Boards | 5 | 100% | 0% | 05-Jul-26 | 09-Jul-26 | 17-Oct-26 | 21-Oct-26 | 0.00 | 0.00 | 0.00 | -88 |
| MLTX-02-005-PR-1 | Material Delivery for Distribution Boards | 15 | 100% | 0% | 11-Jul-26 | 27-Jul-26 | 22-Oct-26 | 08-Nov-26 | 0.00 | 0.00 | 0.00 | -88 |
| **POWER CABLES** | | 15 | 0% | 0% | 11-Jul-26 | 27-Jul-26 | 22-Oct-26 | 08-Nov-26 | 0.00 | 0.00 | 0.00 | -88 |
| MLTX-02-005-PR-1 | PO for Power Cables | 5 | 100% | 0% | 11-Jul-26 | 15-Jul-26 | 22-Oct-26 | 27-Oct-26 | 0.00 | 0.00 | 0.00 | -88 |
| MLTX-02-005-PR-1 | Material Delivery for Power Cables | 10 | 100% | 0% | 16-Jul-26 | 27-Jul-26 | 28-Oct-26 | 08-Nov-26 | 0.00 | 0.00 | 0.00 | -88 |
| **LIGHT FIXTURES** | | 40 | 0% | 0% | 16-Jul-26 | 02-Aug-26 | 07-Jul-26 A | 08-Nov-26 | 0.00 | 0.00 | 0.00 | -83 |
| MLTX-02-005-PR-1 | PO for Light Fixtures | 5 | 100% | 100% | 16-Jul-26 | 21-Jul-26 | 07-Jul-26 A | 07-Jul-26 A | 0.00 | 0.00 | 0.00 | 12 |
| MLTX-02-005-PR-1 | Material Delivery for Light Fixtures | 10 | 100% | 0% | 22-Jul-26 | 02-Aug-26 | 28-Oct-26 | 08-Nov-26 | 0.00 | 0.00 | 0.00 | -83 |
| **CCTV MATERIALS** | | 50 | 0% | 0% | 22-Jul-26 | 29-Aug-26 | 29-Sep-26 | 25-Nov-26 | 0.00 | 0.00 | 0.00 | -75 |
| MLTX-02-005-PR-1 | PO for CCTV | 5 | 100% | 0% | 22-Jul-26 | 27-Jul-26 | 29-Sep-26 | 04-Oct-26 | 0.00 | 0.00 | 0.00 | -58 |
| MLTX-02-005-PR-1 | Material Delivery for CCTV | 15 | 100% | 0% | 12-Aug-26 | 29-Aug-26 | 09-Nov-26 | 25-Nov-26 | 0.00 | 0.00 | 0.00 | -75 |
| **POWER OUTLETS/SWITCHES** | | 21 | 0% | 0% | 28-Jul-26 | 20-Aug-26 | 13-Oct-26 | 05-Nov-26 | 0.00 | 0.00 | 0.00 | -65 |
| MLTX-02-005-PR-1 | PO for Power Outlets/Switches | 6 | 100% | 0% | 28-Jul-26 | 03-Aug-26 | 13-Oct-26 | 19-Oct-26 | 0.00 | 0.00 | 0.00 | -65 |
| MLTX-02-005-PR-1 | Material Delivery for Power Outlets/Switches | 15 | 100% | 0% | 04-Aug-26 | 20-Aug-26 | 20-Oct-26 | 05-Nov-26 | 0.00 | 0.00 | 0.00 | -65 |
| **LANDSCAPE WORKS** | | 124 | 0% | 0% | 04-Aug-26 | 21-Oct-26 | 16-May-26 A | 13-Feb-27 | 0.00 | 0.00 | 0.00 | -98 |
| **INTERLOCKING PAVING** | | 21 | 0% | 0% | 04-Aug-26 | 23-Aug-26 | 26-Aug-26 A | 26-Aug-26 A | 0.00 | 0.00 | 0.00 | -3 |
| MLTX-02-005-PR-1 | PO for Interlocking Block Pavers | 5 | 100% | 100% | 04-Aug-26 | 09-Aug-26 | 26-Aug-26 A | 26-Aug-26 A | 0.00 | 0.00 | 0.00 | -15 |
| MLTX-02-005-PR-1 | Material Delivery for Interlocking Block Pavers | 12 | 100% | 100% | 10-Aug-26 | 23-Aug-26 | 26-Aug-26 A | 26-Aug-26 A | 0.00 | 0.00 | 0.00 | -3 |
| **CURBSTONE** | | 21 | 0% | 0% | 04-Aug-26 | 23-Aug-26 | 14-Jul-26 A | 23-Jul-26 A | 0.00 | 0.00 | 0.00 | 26 |
| MLTX-02-005-PR-1 | PO for Curbstone | 5 | 100% | 100% | 04-Aug-26 | 09-Aug-26 | 14-Jul-26 A | 14-Jul-26 A | 0.00 | 0.00 | 0.00 | 22 |
| MLTX-02-005-PR-1 | Material Delivery for Curbstone | 12 | 100% | 100% | 10-Aug-26 | 23-Aug-26 | 23-Jul-26 A | 23-Jul-26 A | 0.00 | 0.00 | 0.00 | 26 |
| **PAVEMENT MARKING** | | 15 | 0% | 0% | 04-Aug-26 | 20-Aug-26 | 20-Oct-26 | 05-Nov-26 | 0.00 | 0.00 | 0.00 | -65 |
| MLTX-02-005-PR-1 | PO for Pavement Markings | 5 | 100% | 0% | 04-Aug-26 | 09-Aug-26 | 20-Oct-26 | 25-Oct-26 | 0.00 | 0.00 | 0.00 | -65 |
| MLTX-02-005-PR-1 | Material Delivery for Pavement Markings | 10 | 100% | 0% | 10-Aug-26 | 20-Aug-26 | 26-Oct-26 | 05-Nov-26 | 0.00 | 0.00 | 0.00 | -65 |
| **TRAFFIC SIGNS** | | 14 | 0% | 0% | 05-Oct-26 | 20-Oct-26 | 26-Oct-26 | 10-Nov-26 | 0.00 | 0.00 | 0.00 | -18 |
| MLTX-02-005-PR-1 | PO for Traffic Signs | 5 | 0% | 0% | 05-Oct-26 | 10-Oct-26 | 26-Oct-26 | 31-Oct-26 | 0.00 | 0.00 | 0.00 | -18 |
| MLTX-02-005-PR-1 | Material Delivery for Traffic Signs | 9 | 0% | 0% | 11-Oct-26 | 20-Oct-26 | 01-Nov-26 | 10-Nov-26 | 0.00 | 0.00 | 0.00 | -18 |
| **IRRIGATION PIPES/SPRINKLERS** | | 14 | 0% | 0% | 10-Aug-26 | 24-Aug-26 | 26-Oct-26 | 10-Nov-26 | 0.00 | 0.00 | 0.00 | -66 |
| MLTX-02-005-PR-1 | PO for Irrigation Pipes/Sprinkles | 5 | 100% | 0% | 10-Aug-26 | 15-Aug-26 | 26-Oct-26 | 31-Oct-26 | 0.00 | 0.00 | 0.00 | -65 |
| MLTX-02-005-PR-1 | Material Delivery for Irrigation Pipes/Sprinkles | 8 | 100% | 0% | 16-Aug-26 | 24-Aug-26 | 02-Nov-26 | 10-Nov-26 | 0.00 | 0.00 | 0.00 | -66 |
| **AGRICULTURE SOIL** | | 17 | 0% | 0% | 22-Sep-26 | 12-Oct-26 | 21-Jan-27 | 09-Feb-27 | 0.00 | 0.00 | 0.00 | -103 |
| MLTX-02-005-PR-1 | PO for Agriculture Soil | 5 | 100% | 0% | 22-Sep-26 | 28-Sep-26 | 21-Jan-27 | 26-Jan-27 | 0.00 | 0.00 | 0.00 | -103 |
| MLTX-02-005-PR-1 | Material Delivery for Agriculture Soil | 12 | 0% | 0% | 29-Sep-26 | 12-Oct-26 | 27-Jan-27 | 09-Feb-27 | 0.00 | 0.00 | 0.00 | -103 |
| **TRACK SURFACE** | | 24 | 0% | 0% | 05-Sep-26 | 21-Sep-26 | 16-May-26 A | 20-Jan-27 | 0.00 | 0.00 | 0.00 | -103 |
| MLTX-02-005-PR-1 | PO for Track Surface | 5 | 100% | 100% | 05-Sep-26 | 09-Sep-26 | 16-May-26 A | 20-May-26 A | 0.00 | 0.00 | 0.00 | 93 |
| MLTX-02-005-PR-1 | Material Delivery for Track Surface | 10 | 100% | 0% | 10-Sep-26 | 21-Sep-26 | 10-Jan-27 | 20-Jan-27 | 0.00 | 0.00 | 0.00 | -103 |
| **GRASS/TREES** | | 24 | 0% | 0% | 29-Sep-26 | 21-Oct-26 | 17-May-26 A | 13-Feb-27 | 0.00 | 0.00 | 0.00 | -98 |
| MLTX-02-005-PR-1 | PO for Grass/Trees | 5 | 0% | 100% | 29-Sep-26 | 04-Oct-26 | 17-May-26 A | 20-May-26 A | 0.00 | 0.00 | 0.00 | 113 |
| MLTX-02-005-PR-1 | Material Delivery for Grass/Trees | 15 | 0% | 0% | 05-Oct-26 | 21-Oct-26 | 27-Jan-27 | 13-Feb-27 | 0.00 | 0.00 | 0.00 | -98 |
| **CABLES** | | 33 | 0% | 0% | 10-Aug-26 | 01-Sep-26 | 26-Aug-26 A | 15-Sep-26 A | 0.00 | 0.00 | 0.00 | -12 |
| MLTX-02-005-PR-1 | PO for Cables | 5 | 100% | 100% | 10-Aug-26 | 15-Aug-26 | 26-Aug-26 A | 26-Aug-26 A | 0.00 | 0.00 | 0.00 | -10 |
| MLTX-02-005-PR-1 | Material Delivery for Cables | 15 | 100% | 100% | 16-Aug-26 | 01-Sep-26 | 15-Sep-26 A | 15-Sep-26 A | 0.00 | 0.00 | 0.00 | -12 |
| **LONG LEAD ITEM** | | 93 | 0% | 0% | 21-May-26 | 08-Nov-26 | 26-Aug-26 A | 09-Jan-27 | 0.00 | 0.00 | 0.00 | -53 |
| **PLAYGROUND WORKS** | | 88 | 0% | 0% | 21-May-26 | 03-Sep-26 | 29-Sep-26 | 09-Jan-27 | 0.00 | 0.00 | 0.00 | -108 |
| **STEEL TENSION CABLES** | | 65 | 0% | 0% | 21-May-26 | 08-Aug-26 | 29-Sep-26 | 13-Dec-26 | 0.00 | 0.00 | 0.00 | -108 |
| MLTX-02-005-PR-1 | PO for Steel Tension Cables | 8 | 100% | 0% | 21-May-26 | 02-Jun-26 | 29-Sep-26 | 07-Oct-26 | 0.00 | 0.00 | 0.00 | -108 |
| MLTX-02-005-PR-1 | Material Delivery for Steel Tension Cables | 30 | 100% | 0% | 27-Jun-26 | 30-Jul-26 | 01-Nov-26 | 05-Dec-26 | 0.00 | 0.00 | 0.00 | -108 |
| MLTX-02-005-PR-1 | Material Fabrication for Steel Tension Cables | 20 | 100% | 0% | 03-Jun-26 | 25-Jun-26 | 08-Oct-26 | 31-Oct-26 | 0.00 | 0.00 | 0.00 | -108 |
| MLTX-02-005-PR-1 | Staging time | 7 | 100% | 0% | 01-Aug-26 | 08-Aug-26 | 06-Dec-26 | 13-Dec-26 | 0.00 | 0.00 | 0.00 | -108 |
| **EMERGENCY DOORS** | | 60 | 0% | 0% | 27-Jun-26 | 03-Sep-26 | 01-Nov-26 | 09-Jan-27 | 0.00 | 0.00 | 0.00 | -108 |
| MLTX-02-005-PR-1 | PO for Emergency Doors | 10 | 100% | 0% | 27-Jun-26 | 07-Jul-26 | 01-Nov-26 | 11-Nov-26 | 0.00 | 0.00 | 0.00 | -108 |
| MLTX-02-005-PR-1 | Material Delivery for Emergency Doors | 25 | 100% | 0% | 01-Aug-26 | 29-Aug-26 | 06-Dec-26 | 03-Jan-27 | 0.00 | 0.00 | 0.00 | -108 |
| MLTX-02-005-PR-1 | Material Fabrication for Emergency Doors | 20 | 100% | 0% | 08-Jul-26 | 30-Jul-26 | 12-Nov-26 | 05-Dec-26 | 0.00 | 0.00 | 0.00 | -108 |
| MLTX-02-005-PR-1 | Staging time | 5 | 100% | 0% | 30-Aug-26 | 03-Sep-26 | 04-Jan-27 | 09-Jan-27 | 0.00 | 0.00 | 0.00 | -108 |
| **PRESSURE UNITS** | | 60 | 0% | 0% | 27-Jun-26 | 03-Sep-26 | 01-Nov-26 | 09-Jan-27 | 0.00 | 0.00 | 0.00 | -108 |
| MLTX-02-005-PR-1 | PO for Pressure Units | 10 | 100% | 0% | 27-Jun-26 | 07-Jul-26 | 01-Nov-26 | 11-Nov-26 | 0.00 | 0.00 | 0.00 | -108 |
| MLTX-02-005-PR-1 | Material Delivery for Pressure Units | 25 | 100% | 0% | 01-Aug-26 | 29-Aug-26 | 06-Dec-26 | 03-Jan-27 | 0.00 | 0.00 | 0.00 | -108 |
| MLTX-02-005-PR-1 | Material Fabrication for Pressure Units | 20 | 100% | 0% | 08-Jul-26 | 30-Jul-26 | 12-Nov-26 | 05-Dec-26 | 0.00 | 0.00 | 0.00 | -108 |
| MLTX-02-005-PR-1 | Staging time | 5 | 100% | 0% | 30-Aug-26 | 03-Sep-26 | 04-Jan-27 | 09-Jan-27 | 0.00 | 0.00 | 0.00 | -108 |
| **AIR LOCK DOORS** | | 60 | 0% | 0% | 27-Jun-26 | 03-Sep-26 | 01-Nov-26 | 09-Jan-27 | 0.00 | 0.00 | 0.00 | -108 |

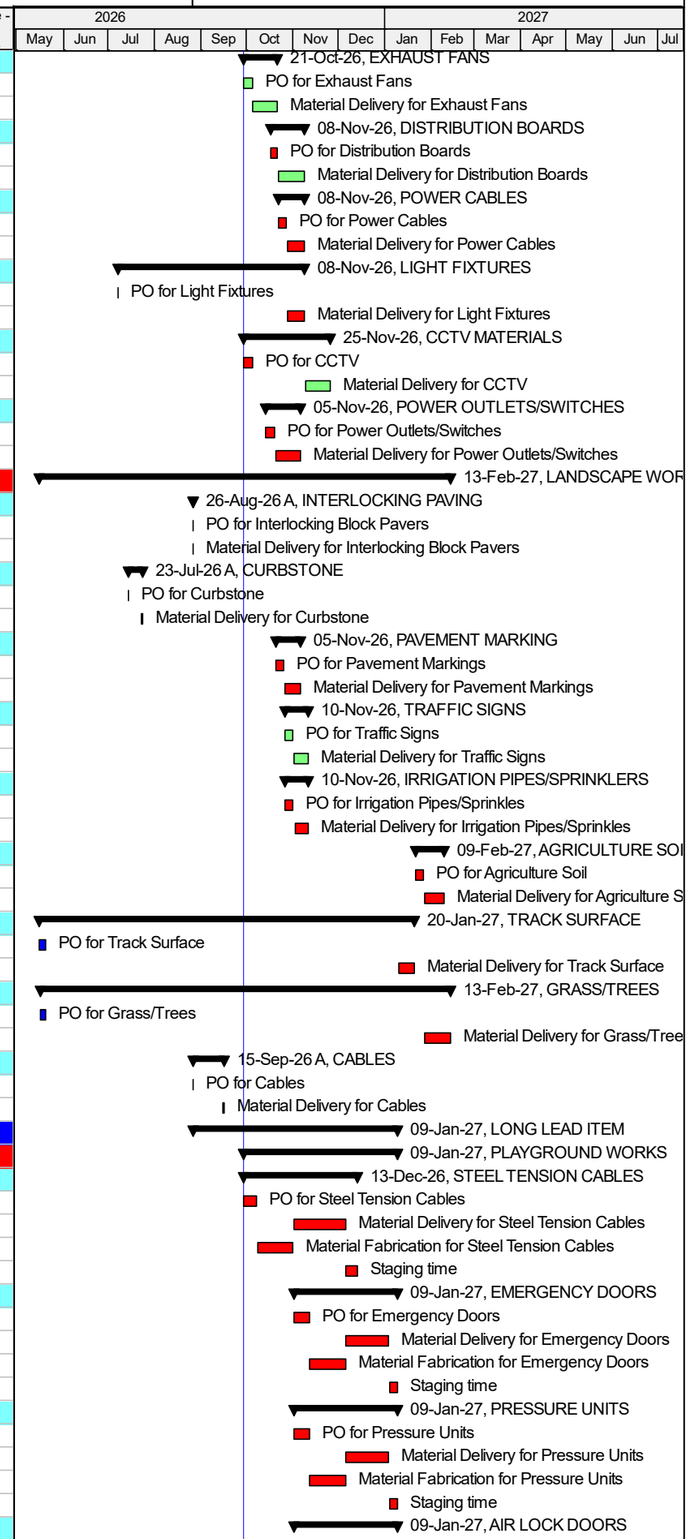


Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary




TASK filter: All Activities

© Oracle Corporation

# MLTX-02-005 - Playground Initiative for Eastern Region (Arar-Hasa osis -Dammam)

**Updateded schedule**
**D.D 28-09-2026**

| Activity ID | Activity Name | Original Duration | Schedule % Complete | Performance % Complete | BL Project Start | BL Project Finish | Start | Finish | Planned Value Cost | Earned Value Cost | Budgeted Total Cost | Variance - BL Project |
|---|---|---|---|---|---|---|---|---|---|---|---|---|
| MLTX-02-005-PR-1 | PO for Lock Doors | 10 | 100% | 0% | 27-Jun-26 | 07-Jul-26 | 01-Nov-26 | 11-Nov-26 | 0.00 | 0.00 | 0.00 | -108 |
| MLTX-02-005-PR-1 | Material Delivery for Lock Doors | 25 | 100% | 0% | 01-Aug-26 | 29-Aug-26 | 06-Dec-26 | 03-Jan-27 | 0.00 | 0.00 | 0.00 | -108 |
| MLTX-02-005-PR-1 | Material Fabrication for Lock Doors | 20 | 100% | 0% | 08-Jul-26 | 30-Jul-26 | 12-Nov-26 | 05-Dec-26 | 0.00 | 0.00 | 0.00 | -108 |
| MLTX-02-005-PR-1 | Staging time | 5 | 100% | 0% | 30-Aug-26 | 03-Sep-26 | 04-Jan-27 | 09-Jan-27 | 0.00 | 0.00 | 0.00 | -108 |
| **LANDSCAPE WORKS** | | 89 | 0% | 0% | 16-Aug-26 | 08-Nov-26 | 26-Aug-26 A | 15-Sep-26 A | 0.00 | 0.00 | 0.00 | 45 |
| **LIGHT POLES** | | 89 | 0% | 0% | 16-Aug-26 | 08-Nov-26 | 26-Aug-26 A | 15-Sep-26 A | 0.00 | 0.00 | 0.00 | 45 |
| MLTX-02-005-PR-1 | PO for Lighting poles | 10 | 100% | 100% | 16-Aug-26 | 26-Aug-26 | 26-Aug-26 A | 26-Aug-26 A | 0.00 | 0.00 | 0.00 | 0 |
| MLTX-02-005-PR-1 | Material Fabrication for Lighting poles | 30 | 83.33% | 100% | 30-Aug-26 | 04-Oct-26 | 26-Aug-26 A | 26-Aug-26 A | 0.00 | 0.00 | 0.00 | 32 |
| MLTX-02-005-PR-1 | Material Delivery for Lighting poles | 25 | 0% | 100% | 05-Oct-26 | 02-Nov-26 | 15-Sep-26 A | 15-Sep-26 A | 0.00 | 0.00 | 0.00 | 40 |
| MLTX-02-005-PR-1 | Staging time | 5 | 0% | 100% | 03-Nov-26 | 08-Nov-26 | 15-Sep-26 A | 15-Sep-26 A | 0.00 | 0.00 | 0.00 | 45 |
| **CONSTRUCTION PHASE** | | 240 | 48.19% | 35.08% | 16-Apr-26 | 29-Dec-26 | 04-Apr-26 A | 08-Apr-27 | 4,772,983.34 | 3,474,412.25 | 9,904,307.16 | -82 |
| **SITE WORKS** | | 240 | 41.67% | 31.7% | 16-Apr-26 | 29-Dec-26 | 04-Apr-26 A | 08-Apr-27 | 3,627,240.60 | 2,759,479.99 | 8,704,943.25 | -82 |
| **EARTH WORKS** | | 66 | 100% | 100% | 16-Apr-26 | 31-May-26 | 04-Apr-26 A | 13-Aug-26 A | 947,872.24 | 947,872.24 | 947,872.24 | -63 |
| MLTX-02-005-CN-133 | Excavation (in all types of soil) including Compaction | 12 | 100% | 100% | 27-Apr-26 | 10-May-26 | 06-Apr-26 A | 12-Apr-26 A | 167,998.20 | 167,998.20 | 167,998.20 | 24 |
| MLTX-02-005-CN-133 | Excavation (in all types of soil) including Compaction | 9 | 100% | 100% | 16-Apr-26 | 26-Apr-26 | 04-Apr-26 A | 02-Aug-26 A | 350,569.48 | 350,569.48 | 350,569.48 | -81 |
| MLTX-02-005-CN-133 | Excavation (in all types of soil) including Compaction | 7 | 100% | 100% | 11-May-26 | 18-May-26 | 06-Apr-26 A | 05-Aug-26 A | 132,864.45 | 132,864.45 | 132,864.45 | -64 |
| MLTX-02-005-CN-133 | Backfilling on Layers (Selected Soil) including Compaction | 10 | 100% | 100% | 11-May-26 | 21-May-26 | 13-Apr-26 A | 30-Apr-26 A | 118,662.34 | 118,662.34 | 118,662.34 | 19 |
| MLTX-02-005-CN-133 | Backfilling on Layers (Selected Soil) including Compaction | 20 | 100% | 100% | 27-Apr-26 | 19-May-26 | 06-Apr-26 A | 08-Apr-26 A | 76,629.23 | 76,629.23 | 76,629.23 | 35 |
| MLTX-02-005-CN-133 | Backfilling on Layers (Selected Soil) including Compaction | 8 | 100% | 100% | 19-May-26 | 31-May-26 | 21-Apr-26 A | 13-Aug-26 A | 101,148.54 | 101,148.54 | 101,148.54 | -63 |
| **LANDSCAPE WORKS** | | 223 | 34.8% | 22.77% | 23-May-26 | 29-Dec-26 | 19-May-26 A | 08-Apr-27 | 2,679,368.36 | 1,753,114.43 | 7,698,577.68 | -82 |
| **PLAYGROUND AREA** | | 213 | 69.28% | 53.64% | 23-May-26 | 08-Dec-26 | 19-May-26 A | 28-Mar-27 | 913,960.35 | 707,562.27 | 1,319,195.08 | -90 |
| **FOOTBALL PLAYGROUND** | | 205 | 87.38% | 35% | 23-May-26 | 11-Nov-26 | 19-May-26 A | 18-Mar-27 | 276,866.54 | 110,897.50 | 316,849.99 | -105 |
| MLTX-02-005-CI | Preparation and Proofing for Subgrade (Football Playground) | 10 | 100% | 100% | 23-May-26 | 06-Jun-26 | 19-May-26 A | 31-May-26 A | 79,212.50 | 79,212.50 | 79,212.50 | 5 |
| MLTX-02-005-CI | Backfilling and Compaction of Base Layers (Football | 16 | 100% | 100% | 25-Jun-26 | 13-Jul-26 | 01-Jun-26 A | 18-Jun-26 A | 15,842.50 | 15,842.50 | 15,842.50 | 22 |
| MLTX-02-005-CI | Finishing Asphalt & Concrete Surface (Football Playground) | 20 | 100% | 0% | 24-Aug-26 | 15-Sep-26 | 07-Nov-26 | 29-Nov-26 | 158,424.99 | 0.00 | 158,424.99 | -63 |
| MLTX-02-005-CI | Install Sport Equipments - Goal / Nets - (Football Playground) | 5 | 0% | 0% | 07-Nov-26 | 11-Nov-26 | 14-Mar-27 | 18-Mar-27 | 0.00 | 0.00 | 31,685.00 | -105 |
| MLTX-02-005-CI | Surface Marking and Painting (Football Playground) | 21 | 47.62% | 0% | 16-Sep-26 | 11-Oct-26 | 30-Nov-26 | 23-Dec-26 | 7,544.05 | 0.00 | 15,842.50 | -63 |
| MLTX-02-005-CI | Aggregate basecourse layer (Football Playground) | 21 | 100% | 100% | 14-Jul-26 | 06-Aug-26 | 20-Jun-26 A | 28-Jun-26 A | 15,842.50 | 15,842.50 | 15,842.50 | 35 |
| **PADEL PLAYGROUND** | | 184 | 70% | 70% | 07-Jun-26 | 11-Nov-26 | 19-May-26 A | 18-Mar-27 | 163,788.80 | 163,788.80 | 233,984.00 | -105 |
| MLTX-02-005-CI | Preparation and Proofing for Subgrade (Padel Playground) | 7 | 100% | 100% | 07-Jun-26 | 14-Jun-26 | 19-May-26 A | 31-May-26 A | 81,894.40 | 81,894.40 | 81,894.40 | 12 |
| MLTX-02-005-CI | Backfilling and Compaction of Base Layers (Padel | 16 | 100% | 100% | 25-Jun-26 | 13-Jul-26 | 01-Jun-26 A | 18-Jun-26 A | 11,699.20 | 11,699.20 | 11,699.20 | 22 |
| MLTX-02-005-CI | Finishing Asphalt & Concrete Surface (Padel Playground) | 21 | 100% | 100% | 01-Sep-26 | 26-Sep-26 | 24-Aug-26 A | 25-Aug-26 A | 58,496.00 | 58,496.00 | 58,496.00 | 26 |
| MLTX-02-005-CI | Install Sport Equipments - Goal / Nets - (Padel Playground) | 5 | 0% | 0% | 07-Nov-26 | 11-Nov-26 | 14-Mar-27 | 18-Mar-27 | 0.00 | 0.00 | 58,496.00 | -105 |
| MLTX-02-005-CI | Surface Marking and Painting (Padel Playground) | 5 | 0% | 0% | 07-Nov-26 | 11-Nov-26 | 14-Mar-27 | 18-Mar-27 | 0.00 | 0.00 | 11,699.20 | -105 |
| MLTX-02-005-CI | Aggregate basecourse layer (Padel Playground) | 21 | 100% | 100% | 08-Aug-26 | 31-Aug-26 | 20-Jun-26 A | 28-Jun-26 A | 11,699.20 | 11,699.20 | 11,699.20 | 56 |
| **BASKETBALL PLAYGROUND** | | 171 | 42.32% | 70% | 15-Jun-26 | 21-Nov-26 | 19-May-26 A | 28-Mar-27 | 136,788.67 | 226,230.90 | 323,187.00 | -105 |
| MLTX-02-005-CI | Preparation and Proofing for Subgrade (Basketball | 10 | 100% | 100% | 15-Jun-26 | 25-Jun-26 | 19-May-26 A | 31-May-26 A | 95,055.00 | 95,055.00 | 95,055.00 | 22 |
| MLTX-02-005-CI | Backfilling and Compaction of Base Layers (Basketball | 11 | 100% | 100% | 01-Jul-26 | 13-Jul-26 | 01-Jun-26 A | 18-Jun-26 A | 16,159.35 | 16,159.35 | 16,159.35 | 22 |
| MLTX-02-005-CI | Finishing Asphalt & Concrete Surface (Basketball | 21 | 9.52% | 100% | 27-Sep-26 | 20-Oct-26 | 20-Aug-26 A | 25-Aug-26 A | 9,414.97 | 98,857.20 | 98,857.20 | 47 |
| MLTX-02-005-CI | Install Sport Equipments - Goal / Nets - (Basketball | 8 | 0% | 0% | 12-Nov-26 | 21-Nov-26 | 20-Mar-27 | 28-Mar-27 | 0.00 | 0.00 | 80,796.75 | -105 |
| MLTX-02-005-CI | Surface Marking and Painting (Basketball Playground) | 8 | 0% | 0% | 12-Nov-26 | 21-Nov-26 | 20-Mar-27 | 28-Mar-27 | 0.00 | 0.00 | 16,159.35 | -105 |
| MLTX-02-005-CI | Aggregate basecourse layer (Basketball Playground) | 21 | 100% | 100% | 01-Sep-26 | 26-Sep-26 | 20-Jun-26 A | 28-Jun-26 A | 16,159.35 | 16,159.35 | 16,159.35 | 77 |
| **PADEL FENCE** | | 153 | 0% | 30% | 22-Nov-26 | 08-Dec-26 | 08-Aug-26 A | 05-Nov-26 | 0.00 | 24,860.73 | 82,869.08 | 28 |
| MLTX-02-005-CI | Excavation for Fence | 8 | 0% | 100% | 22-Nov-26 | 30-Nov-26 | 08-Aug-26 A | 08-Aug-26 A | 0.00 | 8,286.91 | 8,286.91 | 97 |
| MLTX-02-005-CI | Concrete Foundation for Fence including Posts Fixation | 7 | 0% | 100% | 22-Nov-26 | 29-Nov-26 | 15-Aug-26 A | 23-Aug-26 A | 0.00 | 16,573.82 | 16,573.82 | 83 |
| MLTX-02-005-CI | Backfilling and Reinstatement for Concrete Foundation | 6 | 0% | 0% | 22-Nov-26 | 28-Nov-26 | 20-Oct-26 | 26-Oct-26 | 0.00 | 0.00 | 4,143.45 | 28 |
| MLTX-02-005-CI | Tempered Glass Fenc Installation and Fixation | 15 | 0% | 0% | 22-Nov-26 | 08-Dec-26 | 20-Oct-26 | 05-Nov-26 | 0.00 | 0.00 | 33,147.63 | 28 |
| MLTX-02-005-CI | Chain Link Fence Installation and Fixation | 15 | 0% | 0% | 22-Nov-26 | 08-Dec-26 | 20-Oct-26 | 05-Nov-26 | 0.00 | 0.00 | 16,573.82 | 28 |
| MLTX-02-005-CI | Install of Fence Gates | 15 | 0% | 0% | 22-Nov-26 | 08-Dec-26 | 20-Oct-26 | 05-Nov-26 | 0.00 | 0.00 | 4,143.45 | 28 |
| **CURBSTOEN/INTERLOCK** | | 62 | 92.88% | 50.17% | 12-Aug-26 | 01-Oct-26 | 10-Aug-26 A | 30-Nov-26 | 336,516.34 | 181,784.34 | 362,305.01 | -51 |
| MLTX-02-005-CI | Interlock Installation (Grey Scale) for LandScape (Including | 21 | 85.71% | 0% | 07-Sep-26 | 01-Oct-26 | 07-Nov-26 | 30-Nov-26 | 154,732.00 | 0.00 | 180,520.67 | -51 |
| MLTX-02-005-CI | Concrete Works Under Curbstone | 3 | 100% | 100% | 12-Aug-26 | 15-Aug-26 | 10-Aug-26 A | 10-Aug-26 A | 54,535.30 | 54,535.30 | 54,535.30 | 4 |
| MLTX-02-005-CI | Curbstone Installation | 4 | 100% | 100% | 02-Sep-26 | 06-Sep-26 | 11-Aug-26 A | 13-Aug-26 A | 127,249.04 | 127,249.04 | 127,249.04 | 20 |
| **AIR DOME** | | 184 | 33.89% | 11.91% | 14-Jul-26 | 24-Nov-26 | 14-Jul-26 A | 08-Apr-27 | 1,654,201.74 | 581,544.30 | 4,881,359.87 | -112 |
| **CIVIL WORKS** | | 113 | 84.13% | 29.58% | 14-Jul-26 | 04-Oct-26 | 14-Jul-26 A | 25-Nov-26 | 1,654,201.74 | 581,544.30 | 1,966,294.68 | -45 |
| MLTX-02-005-CI | Excavation for Foundation (Air Dome) | 10 | 100% | 100% | 14-Jul-26 | 25-Jul-26 | 14-Jul-26 A | 02-Aug-26 A | 127,762.34 | 127,762.34 | 127,762.34 | -7 |
| MLTX-02-005-CI | Concrete Works for Foundations including Anchor Bolts (Air | 15 | 100% | 100% | 26-Jul-26 | 11-Aug-26 | 10-Aug-26 A | 21-Sep-26 A | 168,176.84 | 168,176.84 | 168,176.84 | -35 |
| MLTX-02-005-CI | Cable System Installation (Air Dome) | 10 | 100% | 100% | 12-Aug-26 | 23-Aug-26 | 21-Sep-26 A | 21-Sep-26 A | 41,790.29 | 41,790.29 | 41,790.29 | -25 |
| MLTX-02-005-CI | Install of Membrane Covering System (Air Dome) | 15 | 66.67% | 0% | 16-Sep-26 | 04-Oct-26 | 09-Nov-26 | 25-Nov-26 | 624,185.87 | 0.00 | 936,278.81 | -45 |
| MLTX-02-005-CI | Thermal Insulation Works (Air Dome) | 10 | 100% | 0% | 16-Sep-26 | 28-Sep-26 | 09-Nov-26 | 19-Nov-26 | 448,471.57 | 0.00 | 448,471.57 | -45 |
| MLTX-02-005-CI | Perimeter Clamping System Installation | 10 | 100% | 100% | 05-Sep-26 | 15-Sep-26 | 21-Sep-26 A | 28-Sep-26 A | 243,814.83 | 243,814.83 | 243,814.83 | -10 |
| **MECHANICAL WORKS** | | 33 | 0% | 0% | 29-Sep-26 | 05-Nov-26 | 30-Jan-27 | 09-Mar-27 | 0.00 | 0.00 | 1,233,296.81 | -105 |
| MLTX-02-005-CI | Air Ducts and Grills Installation (Air Dome) | 10 | 0% | 0% | 29-Sep-26 | 10-Oct-26 | 30-Jan-27 | 09-Feb-27 | 0.00 | 0.00 | 728,766.30 | -105 |
| MLTX-02-005-CI | Air Units Installation (Air Dome) | 13 | 0% | 0% | 11-Oct-26 | 25-Oct-26 | 10-Feb-27 | 25-Feb-27 | 0.00 | 0.00 | 336,353.67 | -105 |

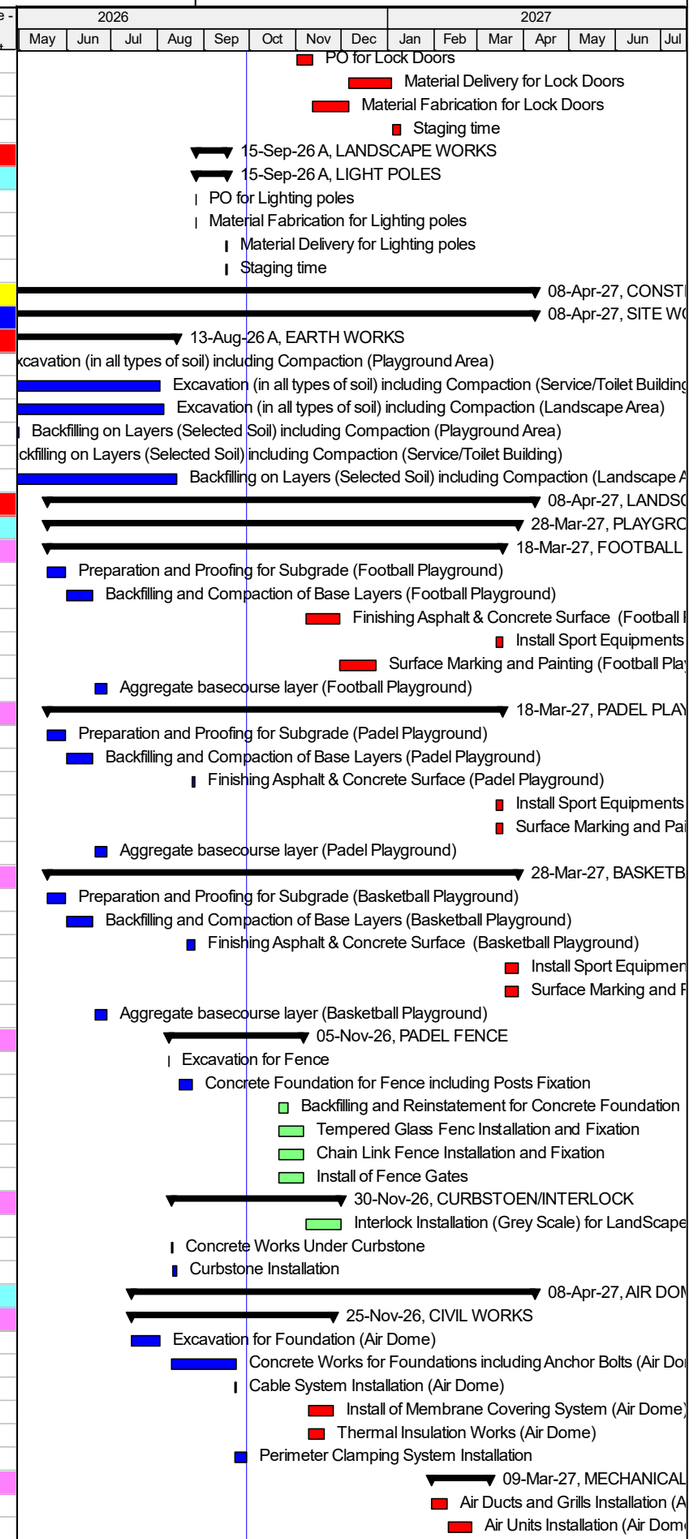


Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary




TASK filter: All Activities

© Oracle Corporation

# MLTX-02-005 - Playground Initiative for Eastern Region (Arar-Hasa osis -Dammam)

**Updateded schedule**
**D.D 28-09-2026**

| Activity ID | Activity Name | Original Duration | Schedule % Complete | Performance % Complete | BL Project Start | BL Project Finish | Start | Finish | Planned Value Cost | Earned Value Cost | Budgeted Total Cost | Variance - BL Project |
|---|---|---|---|---|---|---|---|---|---|---|---|---|
| MLTX-02-005-CI | Exhaust Fans and Ducts Installation (Air Dome) | 10 | 0% | 0% | 26-Oct-26 | 05-Nov-26 | 27-Feb-27 | 09-Mar-27 | 0.00 | 0.00 | 168,176.84 | -105 |
| **ELECTRICAL WORKS** | | 39 | 0% | 0% | 11-Oct-26 | 24-Nov-26 | 10-Feb-27 | 31-Mar-27 | 0.00 | 0.00 | 1,513,591.54 | -105 |
| MLTX-02-005-CI | Light Fixture Works (Air Dome) | 10 | 0% | 0% | 11-Oct-26 | 21-Oct-26 | 10-Feb-27 | 21-Feb-27 | 0.00 | 0.00 | 224,235.78 | -105 |
| MLTX-02-005-CI | Distribution Board and Electrical Works (Air Dome) | 7 | 0% | 0% | 22-Oct-26 | 29-Oct-26 | 23-Feb-27 | 02-Mar-27 | 0.00 | 0.00 | 168,176.84 | -105 |
| MLTX-02-005-CI | External Electrical Connection Works (Air Dome) | 6 | 0% | 0% | 31-Oct-26 | 05-Nov-26 | 03-Mar-27 | 09-Mar-27 | 0.00 | 0.00 | 168,176.84 | -105 |
| MLTX-02-005-CI | Emergency Generator Installation (Air Dome) | 11 | 0% | 0% | 07-Nov-26 | 18-Nov-26 | 14-Mar-27 | 25-Mar-27 | 0.00 | 0.00 | 504,530.51 | -105 |
| MLTX-02-005-CI | Control System Installation (Air Dome) | 5 | 0% | 0% | 19-Nov-26 | 24-Nov-26 | 27-Mar-27 | 31-Mar-27 | 0.00 | 0.00 | 448,471.57 | -105 |
| **FINISHES WORKS** | | 29 | 0% | 0% | 31-Oct-26 | 22-Nov-26 | 03-Mar-27 | 08-Apr-27 | 0.00 | 0.00 | 168,176.84 | -114 |
| MLTX-02-005-CI | Doors Installation Including Emergency, Entrance doors (Air | 10 | 0% | 0% | 31-Oct-26 | 10-Nov-26 | 03-Mar-27 | 17-Mar-27 | 0.00 | 0.00 | 112,117.89 | -105 |
| MLTX-02-005-CI | Logo and Signs Installation (Air Dome) | 10 | 0% | 0% | 11-Nov-26 | 22-Nov-26 | 29-Mar-27 | 08-Apr-27 | 0.00 | 0.00 | 56,058.95 | -114 |
| **IRRIGATION NETWORK** | | 46 | 23.45% | 73.86% | 27-Sep-26 | 14-Oct-26 | 24-Aug-26 A | 11-Feb-27 | 35,746.67 | 112,570.94 | 152,414.87 | -103 |
| MLTX-02-005-CN-1 | Installing of HDPE Pipes for Irrigation Network (Main Line) | 3 | 66.67% | 100% | 27-Sep-26 | 29-Sep-26 | 24-Aug-26 A | 14-Sep-26 A | 35,746.67 | 53,620.00 | 53,620.00 | 12 |
| MLTX-02-005-CN-1 | Installing of HDPE Pipes for Irrigation Network (Branch Lines) | 3 | 0% | 80% | 30-Sep-26 | 03-Oct-26 | 19-Sep-26 A | 01-Oct-26 | 0.00 | 40,102.26 | 50,127.83 | 1 |
| MLTX-02-005-CN-1 | Installing of Valves and fittings for Irrigation Network | 3 | 0% | 80% | 04-Oct-26 | 06-Oct-26 | 19-Sep-26 A | 01-Oct-26 | 0.00 | 18,848.67 | 23,560.84 | 4 |
| MLTX-02-005-CN-1 | Installing of Bubblers and Spreyers | 2 | 0% | 0% | 13-Oct-26 | 14-Oct-26 | 10-Feb-27 | 11-Feb-27 | 0.00 | 0.00 | 25,106.20 | -103 |
| **NATURAL GROUND** | | 30 | 0% | 0% | 07-Oct-26 | 10-Nov-26 | 14-Oct-26 | 17-Nov-26 | 0.00 | 0.00 | 191,740.00 | -6 |
| MLTX-02-005-CN-1 | Tartan Floor Installation Works for Landscape (Including | 15 | 0% | 0% | 25-Oct-26 | 10-Nov-26 | 01-Nov-26 | 17-Nov-26 | 0.00 | 0.00 | 126,740.00 | -6 |
| MLTX-02-005-CN-1 | Compacted Natural Ground Soil Installation Works for | 15 | 0% | 0% | 07-Oct-26 | 24-Oct-26 | 14-Oct-26 | 31-Oct-26 | 0.00 | 0.00 | 65,000.00 | -6 |
| **PLANTING** | | 23 | 0% | 0% | 15-Oct-26 | 10-Nov-26 | 13-Feb-27 | 15-Mar-27 | 0.00 | 0.00 | 347,251.46 | -103 |
| MLTX-02-005-CN-1 | Placement of Sweet/Agricultural Soil (Including Levelling and | 6 | 0% | 0% | 15-Oct-26 | 21-Oct-26 | 13-Feb-27 | 18-Feb-27 | 0.00 | 0.00 | 104,175.44 | -103 |
| MLTX-02-005-CN-1 | Placement of Lawn Ground Cover (Rolling and Compaction) | 7 | 0% | 0% | 03-Nov-26 | 10-Nov-26 | 04-Mar-27 | 15-Mar-27 | 0.00 | 0.00 | 141,732.50 | -103 |
| MLTX-02-005-CN-1 | Placement and Fixation of Trees | 10 | 0% | 0% | 22-Oct-26 | 02-Nov-26 | 20-Feb-27 | 03-Mar-27 | 0.00 | 0.00 | 101,343.52 | -103 |
| **WALKING/BIKE PATHS** | | 10 | 0% | 100% | 11-Nov-26 | 22-Nov-26 | 19-Jul-26 A | 16-Sep-26 A | 0.00 | 336,345.00 | 336,345.00 | 56 |
| MLTX-02-005-CN-1 | Bike Path Preparation and Installation Works | 10 | 0% | 100% | 11-Nov-26 | 22-Nov-26 | 19-Jul-26 A | 16-Sep-26 A | 0.00 | 171,909.67 | 171,909.67 | 56 |
| MLTX-02-005-CN-1 | Walking Path Preparation and Installation Works | 10 | 0% | 100% | 11-Nov-26 | 22-Nov-26 | 19-Jul-26 A | 16-Sep-26 A | 0.00 | 164,435.33 | 164,435.33 | 56 |
| **GENERAL/FURNITURE** | | 159 | 16.05% | 3.21% | 07-Sep-26 | 29-Dec-26 | 20-Sep-26 A | 06-Apr-27 | 75,459.60 | 15,091.92 | 470,271.40 | -80 |
| MLTX-02-005-CN-1 | Stamped Concrete Works for LandScape (Including | 8 | 0% | 0% | 23-Nov-26 | 01-Dec-26 | 29-Sep-26 | 07-Oct-26 | 0.00 | 0.00 | 93,594.00 | 47 |
| MLTX-02-005-CN-1 | Traffic Signs Posts and Poles Installation | 9 | 0% | 0% | 20-Dec-26 | 29-Dec-26 | 28-Mar-27 | 06-Apr-27 | 0.00 | 0.00 | 9,749.30 | -80 |
| MLTX-02-005-CN-1 | Fixation and Installation of Steel Frame for Benches | 8 | 0% | 0% | 23-Nov-26 | 01-Dec-26 | 29-Sep-26 | 07-Oct-26 | 0.00 | 0.00 | 17,274.79 | 47 |
| MLTX-02-005-CN-1 | Fixation and Installation of Benches | 10 | 0% | 0% | 02-Dec-26 | 13-Dec-26 | 08-Oct-26 | 19-Oct-26 | 0.00 | 0.00 | 40,307.84 | 47 |
| MLTX-02-005-CN-1 | Fixation and Installation of Precast Concrete Seats | 10 | 0% | 0% | 02-Dec-26 | 13-Dec-26 | 08-Oct-26 | 19-Oct-26 | 0.00 | 0.00 | 32,757.76 | 47 |
| MLTX-02-005-CN-1 | Fixation and Installation of Precast Concrete Seats (Circular) | 10 | 0% | 0% | 02-Dec-26 | 13-Dec-26 | 08-Oct-26 | 19-Oct-26 | 0.00 | 0.00 | 12,869.04 | 47 |
| MLTX-02-005-CN-1 | Fixation and Installation of Precast Concrete Trash Bins | 8 | 0% | 0% | 20-Dec-26 | 28-Dec-26 | 20-Oct-26 | 28-Oct-26 | 0.00 | 0.00 | 12,186.67 | 52 |
| MLTX-02-005-CN-1 | Preleminary Works for Site Light Poles Including Cable and | 13 | 100% | 20% | 07-Sep-26 | 21-Sep-26 | 20-Sep-26 A | 13-Oct-26 | 75,459.60 | 15,091.92 | 75,459.60 | -18 |
| MLTX-02-005-CN-1 | Installing of Site Light Poles | 10 | 0% | 0% | 02-Dec-26 | 13-Dec-26 | 16-Mar-27 | 27-Mar-27 | 0.00 | 0.00 | 176,072.40 | -85 |
| **PARKING** | | 145 | 0% | 100% | 02-Dec-26 | 19-Dec-26 | 18-Jul-26 A | 19-Sep-26 A | 0.00 | 58,493.33 | 58,493.33 | 77 |
| MLTX-02-005-CN-133 | Interlock Installation (8 Cm) for Parking Area (Including | 11 | 0% | 100% | 07-Dec-26 | 19-Dec-26 | 10-Sep-26 A | 19-Sep-26 A | 0.00 | 40,945.33 | 40,945.33 | 77 |
| MLTX-02-005-CN-133 | Site Preparation & Compaction Under Interlock for Parking | 4 | 0% | 100% | 02-Dec-26 | 06-Dec-26 | 18-Jul-26 A | 18-Jul-26 A | 0.00 | 17,548.00 | 17,548.00 | 120 |
| **TOILET/SERVICE BUILDING** | | 110 | 95.53% | 59.61% | 01-Jun-26 | 11-Oct-26 | 23-May-26 A | 21-Nov-26 | 1,145,742.74 | 714,932.25 | 1,199,363.91 | -35 |
| **STRUCTURE WORKS** | | 97 | 100% | 100% | 01-Jun-26 | 21-Jul-26 | 23-May-26 A | 02-Aug-26 A | 194,188.64 | 194,188.64 | 194,188.64 | -10 |
| **CONCRETE WORKS** | | 87 | 100% | 100% | 20-Jun-26 | 21-Jul-26 | 25-May-26 A | 27-Jun-26 A | 134,099.30 | 134,099.30 | 134,099.30 | 21 |
| **SUB-STRUCTURE** | | 9 | 100% | 100% | 20-Jun-26 | 29-Jun-26 | 25-May-26 A | 07-Jun-26 A | 53,666.80 | 53,666.80 | 53,666.80 | 19 |
| MLTX-02-005-CI | Plain Concrete Under Footing | 4 | 100% | 100% | 20-Jun-26 | 23-Jun-26 | 25-May-26 A | 31-May-26 A | 17,106.85 | 17,106.85 | 17,106.85 | 20 |
| MLTX-02-005-CI | Reinforced Concrete Works for Slab on Grade Including | 5 | 100% | 100% | 24-Jun-26 | 29-Jun-26 | 03-Jun-26 A | 07-Jun-26 A | 36,559.95 | 36,559.95 | 36,559.95 | 19 |
| **SUPER-STRUCTURE** | | 87 | 100% | 100% | 06-Jul-26 | 21-Jul-26 | 20-Jun-26 A | 27-Jun-26 A | 80,432.50 | 80,432.50 | 80,432.50 | 21 |
| MLTX-02-005-CI | AAC Panels Works for Walls | 7 | 100% | 100% | 06-Jul-26 | 13-Jul-26 | 20-Jun-26 A | 20-Jun-26 A | 48,259.50 | 48,259.50 | 48,259.50 | 20 |
| MLTX-02-005-CI | Parpet Works and Lintels | 3 | 100% | 100% | 19-Jul-26 | 21-Jul-26 | 25-Jun-26 A | 27-Jun-26 A | 16,086.50 | 16,086.50 | 16,086.50 | 21 |
| MLTX-02-005-CI | AAC Panels Works for Slabs | 4 | 100% | 100% | 14-Jul-26 | 18-Jul-26 | 21-Jun-26 A | 24-Jun-26 A | 16,086.50 | 16,086.50 | 16,086.50 | 20 |
| **UNDER GROUND SEPTIC TANK** | | 78 | 100% | 100% | 02-Jun-26 | 07-Jul-26 | 01-Jun-26 A | 06-Jul-26 A | 49,852.54 | 49,852.54 | 49,852.54 | 1 |
| MLTX-02-005-CN-1 | Plain Concrete Under Footing | 3 | 100% | 100% | 02-Jun-26 | 04-Jun-26 | 01-Jun-26 A | 06-Jun-26 A | 17,106.85 | 17,106.85 | 17,106.85 | -1 |
| MLTX-02-005-CN-1 | Reinforced Concrete Works for Tank Slab Including | 10 | 100% | 100% | 27-Jun-26 | 07-Jul-26 | 06-Jul-26 A | 06-Jul-26 A | 8,774.37 | 8,774.37 | 8,774.37 | 1 |
| MLTX-02-005-CN-1 | Reinforced Concrete Works for Tank Foundation Including | 8 | 100% | 100% | 06-Jun-26 | 14-Jun-26 | 09-Jun-26 A | 13-Jun-26 A | 7,604.46 | 7,604.46 | 7,604.46 | 1 |
| MLTX-02-005-CN-1 | Reinforced Concrete Works for Tank Walls Including Steel | 10 | 100% | 100% | 15-Jun-26 | 25-Jun-26 | 18-Jun-26 A | 05-Jul-26 A | 16,366.86 | 16,366.86 | 16,366.86 | -8 |
| **THERMAL & MOISTER PROTECTION** | | 62 | 100% | 100% | 01-Jun-26 | 16-Jul-26 | 23-May-26 A | 02-Aug-26 A | 10,236.80 | 10,236.80 | 10,236.80 | -14 |
| **ANTI TERMIT CONTROL** | | 13 | 100% | 100% | 01-Jun-26 | 15-Jun-26 | 23-May-26 A | 03-Jun-26 A | 4,387.50 | 4,387.50 | 4,387.50 | 10 |
| MLTX-02-005-CI | Anti Termite Works Under Foundation | 1 | 100% | 100% | 01-Jun-26 | 01-Jun-26 | 31-May-26 A | 03-Jun-26 A | 1,755.00 | 1,755.00 | 1,755.00 | -2 |
| MLTX-02-005-CI | Anti Termite Works Under Slab on Grade and Grade Beams | 1 | 100% | 100% | 15-Jun-26 | 15-Jun-26 | 23-May-26 A | 24-May-26 A | 2,632.50 | 2,632.50 | 2,632.50 | 16 |
| **POLYETHYLENE SHEET** | | 13 | 100% | 100% | 01-Jun-26 | 15-Jun-26 | 24-May-26 A | 04-Jun-26 A | 2,193.30 | 2,193.30 | 2,193.30 | 9 |
| MLTX-02-005-CI | Water Proofing Under Blinding Concrete (Polythelen Sheet) | 1 | 100% | 100% | 01-Jun-26 | 01-Jun-26 | 31-May-26 A | 04-Jun-26 A | 877.32 | 877.32 | 877.32 | -3 |
| MLTX-02-005-CI | Water Proofing Under Slab on Grade (Polythelen Sheet) | 1 | 100% | 100% | 15-Jun-26 | 15-Jun-26 | 24-May-26 A | 25-May-26 A | 1,315.98 | 1,315.98 | 1,315.98 | 15 |
| **EPOXY** | | 15 | 100% | 100% | 08-Jul-26 | 16-Jul-26 | 11-Jul-26 A | 02-Aug-26 A | 3,656.00 | 3,656.00 | 3,656.00 | -14 |
| MLTX-02-005-CI | Surface Preparation for Epoxy Coating | 3 | 100% | 100% | 08-Jul-26 | 11-Jul-26 | 11-Jul-26 A | 11-Jul-26 A | 1,096.80 | 1,096.80 | 1,096.80 | 0 |
| MLTX-02-005-CI | Epoxy Coating for Walls and Slab of Tank | 5 | 100% | 100% | 12-Jul-26 | 16-Jul-26 | 02-Aug-26 A | 02-Aug-26 A | 2,559.20 | 2,559.20 | 2,559.20 | -14 |
| **MASONARY WORK** | | 5 | 100% | 100% | 30-Jun-26 | 05-Jul-26 | 06-Jul-26 A | 08-Jul-26 A | 12,284.10 | 12,284.10 | 12,284.10 | -3 |

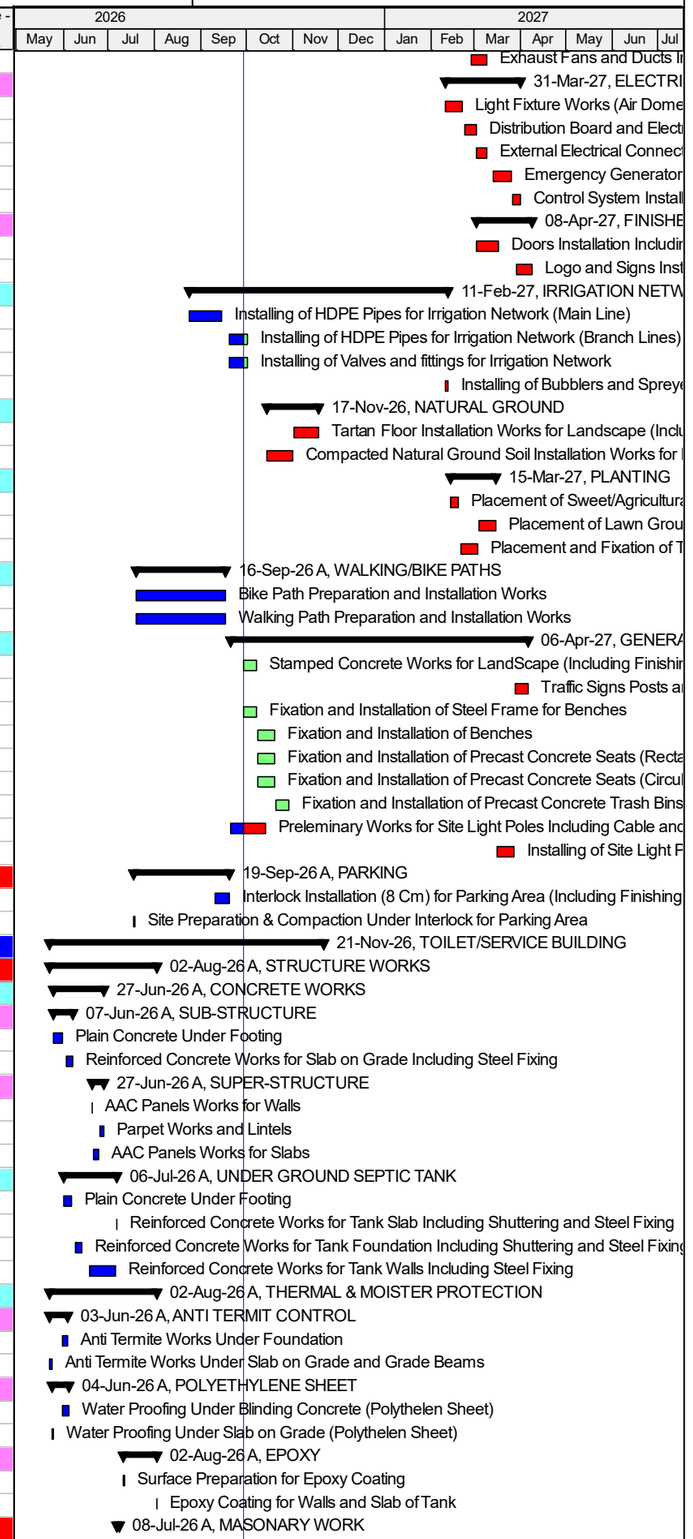





© Oracle Corporation

# MLTX-02-005 - Playground Initiative for Eastern Region (Arar-Hasa osis -Dammam)

**Updateded schedule**
**D.D 28-09-2026**

| Activity ID | Activity Name | Original Duration | Schedule % Complete | Performance % Complete | BL Project Start | BL Project Finish | Start | Finish | Planned Value Cost | Earned Value Cost | Budgeted Total Cost | Variance - BL Project |
|---|---|---|---|---|---|---|---|---|---|---|---|---|
| MLTX-02-005-CN-140 | CMU Masonary Works Including all Accessories | 5 | 100% | 100% | 30-Jun-26 | 05-Jul-26 | 06-Jul-26 A | 08-Jul-26 A | 12,284.10 | 12,284.10 | 12,284.10 | -3 |
| **THERMAL & MOISTER PROTECTION** | | 23 | 100% | 90.43% | 22-Jul-26 | 15-Aug-26 | 25-Aug-26 A | 07-Oct-26 | 34,698.32 | 31,376.86 | 34,698.32 | -45 |
| MLTX-02-005-CN-140 | Preparing Surface and Preliminary Works for Toilets | 2 | 100% | 100% | 22-Jul-26 | 23-Jul-26 | 25-Aug-26 A | 25-Aug-26 A | 2,105.86 | 2,105.86 | 2,105.86 | -28 |
| MLTX-02-005-CN-140 | Finalize Water Proofing Works for Toilets | 5 | 100% | 100% | 25-Jul-26 | 29-Jul-26 | 25-Aug-26 A | 29-Aug-26 A | 4,913.66 | 4,913.66 | 4,913.66 | -26 |
| MLTX-02-005-CN-140 | Preparing Surface and Preliminary Works for Roofing and | 6 | 100% | 100% | 30-Jul-26 | 05-Aug-26 | 05-Sep-26 A | 05-Sep-26 A | 11,071.52 | 11,071.52 | 11,071.52 | -26 |
| MLTX-02-005-CN-140 | Finalize Water Proofing Works for Roofing and Wet Areas | 8 | 100% | 80% | 06-Aug-26 | 15-Aug-26 | 06-Sep-26 A | 07-Oct-26 | 16,607.28 | 13,285.82 | 16,607.28 | -45 |
| **MECHANICAL WORK** | | 46 | 100% | 57.58% | 30-Jul-26 | 20-Sep-26 | 12-Jul-26 A | 31-Oct-26 | 264,673.10 | 152,401.60 | 264,673.10 | -34 |
| **HVAC SYSTEM** | | 32 | 100% | 47.55% | 17-Aug-26 | 19-Sep-26 | 12-Jul-26 A | 31-Oct-26 | 27,883.37 | 13,259.41 | 27,883.37 | -35 |
| MLTX-02-005-CN-1 | Preliminary HVAC and Ventilation Works | 3 | 100% | 100% | 17-Aug-26 | 19-Aug-26 | 12-Jul-26 A | 12-Jul-26 A | 9,359.69 | 9,359.69 | 9,359.69 | 33 |
| MLTX-02-005-CN-1 | Install and Finish HVAC and Ventilation Works Including Split | 3 | 100% | 0% | 16-Sep-26 | 19-Sep-26 | 28-Oct-26 | 31-Oct-26 | 14,623.96 | 0.00 | 14,623.96 | -35 |
| MLTX-02-005-CN-1 | Exhaust, Air Ducts Installation with all Accessories | 6 | 100% | 100% | 20-Aug-26 | 26-Aug-26 | 18-Aug-26 A | 23-Aug-26 A | 3,899.72 | 3,899.72 | 3,899.72 | 3 |
| **WATER SUPPLY SYSTEM** | | 39 | 100% | 65.18% | 02-Aug-26 | 13-Sep-26 | 19-Jul-26 A | 11-Oct-26 | 154,916.69 | 100,970.49 | 154,916.69 | -23 |
| MLTX-02-005-CN-1 | Installing of PPR Pipes and Fittings for Water Network | 3 | 100% | 100% | 02-Aug-26 | 04-Aug-26 | 19-Jul-26 A | 22-Jul-26 A | 6,921.94 | 6,921.94 | 6,921.94 | 11 |
| MLTX-02-005-CN-1 | Installing of HDPE Pipes and Valves for Water Supply | 6 | 100% | 80% | 08-Aug-26 | 13-Aug-26 | 19-Sep-26 A | 05-Oct-26 | 25,998.40 | 20,798.72 | 25,998.40 | -44 |
| MLTX-02-005-CN-1 | Installing of Booster Pump Units Including fittings and | 5 | 100% | 0% | 27-Aug-26 | 01-Sep-26 | 06-Oct-26 | 11-Oct-26 | 48,746.52 | 0.00 | 48,746.52 | -33 |
| MLTX-02-005-CN-1 | Installing of GRP Tanks | 8 | 100% | 100% | 18-Aug-26 | 26-Aug-26 | 06-Sep-26 A | 14-Sep-26 A | 64,995.36 | 64,995.36 | 64,995.36 | -16 |
| MLTX-02-005-CN-1 | Installing of Valves and Fittings | 2 | 100% | 100% | 05-Aug-26 | 06-Aug-26 | 05-Sep-26 A | 05-Sep-26 A | 6,499.60 | 6,499.60 | 6,499.60 | -25 |
| MLTX-02-005-CN-1 | Installing of Water Heater | 4 | 100% | 100% | 09-Sep-26 | 13-Sep-26 | 15-Sep-26 A | 15-Sep-26 A | 1,754.87 | 1,754.87 | 1,754.87 | -2 |
| **SEWER/DRAINAGE SYSTEM** | | 32 | 100% | 47.76% | 30-Jul-26 | 13-Sep-26 | 20-Jul-26 A | 25-Oct-26 | 79,923.17 | 38,171.70 | 79,923.17 | -35 |
| MLTX-02-005-CN-1 | Installing UPVC Pipes for Sewage Network | 2 | 100% | 100% | 30-Jul-26 | 01-Aug-26 | 20-Jul-26 A | 22-Jul-26 A | 11,767.40 | 11,767.40 | 11,767.40 | 8 |
| MLTX-02-005-CN-1 | Installing of Plumping Fixtures and Accessories | 4 | 100% | 0% | 17-Aug-26 | 20-Aug-26 | 29-Sep-26 | 03-Oct-26 | 10,358.68 | 0.00 | 10,358.68 | -36 |
| MLTX-02-005-CN-1 | Installing UPVC Pipes for External Connection for Sewage | 3 | 100% | 100% | 06-Aug-26 | 09-Aug-26 | 26-Sep-26 A | 26-Sep-26 A | 14,217.67 | 14,217.67 | 14,217.67 | -40 |
| MLTX-02-005-CN-1 | Installing Inspection Chamber for Sewage Network | 4 | 100% | 100% | 02-Aug-26 | 05-Aug-26 | 26-Sep-26 A | 26-Sep-26 A | 12,186.63 | 12,186.63 | 12,186.63 | -43 |
| MLTX-02-005-CN-1 | Installing of Toilet Fixtures and Accessories Such as Closets | 4 | 100% | 0% | 09-Sep-26 | 13-Sep-26 | 21-Oct-26 | 25-Oct-26 | 31,392.79 | 0.00 | 31,392.79 | -35 |
| **FIRE PROTECTION** | | 2 | 100% | 0% | 19-Sep-26 | 20-Sep-26 | 29-Sep-26 | 30-Sep-26 | 1,949.87 | 0.00 | 1,949.87 | -8 |
| MLTX-02-005-CN-1 | Installing of Fire Fighting Extinguisher and accessories | 2 | 100% | 0% | 19-Sep-26 | 20-Sep-26 | 29-Sep-26 | 30-Sep-26 | 1,949.87 | 0.00 | 1,949.87 | -8 |
| **ELECTRICAL WORKS** | | 110 | 86.14% | 53.29% | 22-Jul-26 | 11-Oct-26 | 14-Jul-26 A | 21-Nov-26 | 333,377.65 | 206,217.55 | 386,998.82 | -35 |
| **ROUGH-IN WORKS** | | 80 | 100% | 100% | 22-Jul-26 | 25-Jul-26 | 14-Jul-26 A | 17-Aug-26 A | 206,217.55 | 206,217.55 | 206,217.55 | -19 |
| MLTX-02-005-CN-1 | Preleminary Works for Panel Boards | 2 | 100% | 100% | 22-Jul-26 | 23-Jul-26 | 15-Jul-26 A | 22-Jul-26 A | 68,245.12 | 68,245.12 | 68,245.12 | 1 |
| MLTX-02-005-CN-1 | Preleminary Works for Cable Works | 3 | 100% | 100% | 22-Jul-26 | 25-Jul-26 | 14-Jul-26 A | 14-Jul-26 A | 12,488.92 | 12,488.92 | 12,488.92 | 9 |
| MLTX-02-005-CN-1 | Preleminary Works for Sockets and Power Points | 2 | 100% | 100% | 22-Jul-26 | 23-Jul-26 | 14-Jul-26 A | 14-Jul-26 A | 15,990.55 | 15,990.55 | 15,990.55 | 8 |
| MLTX-02-005-CN-1 | Preleminary Works for Lightning Works | 2 | 100% | 100% | 22-Jul-26 | 23-Jul-26 | 28-Jul-26 A | 17-Aug-26 A | 21,935.93 | 21,935.93 | 21,935.93 | -20 |
| MLTX-02-005-CN-1 | Preleminary Works for Data & Telecommunication System | 2 | 100% | 100% | 22-Jul-26 | 23-Jul-26 | 28-Jul-26 A | 17-Aug-26 A | 24,470.75 | 24,470.75 | 24,470.75 | -20 |
| MLTX-02-005-CN-1 | Preleminary Works for Security and Access Control System | 3 | 100% | 100% | 22-Jul-26 | 25-Jul-26 | 28-Jul-26 A | 17-Aug-26 A | 30,913.59 | 30,913.59 | 30,913.59 | -19 |
| MLTX-02-005-CN-1 | Preleminary Works for Earthing Works | 3 | 100% | 100% | 22-Jul-26 | 25-Jul-26 | 28-Jul-26 A | 17-Aug-26 A | 32,172.69 | 32,172.69 | 32,172.69 | -19 |
| **FIXTURE WORKS** | | 46 | 70.34% | 0% | 16-Sep-26 | 11-Oct-26 | 29-Sep-26 | 21-Nov-26 | 127,160.10 | 0.00 | 180,781.27 | -35 |
| MLTX-02-005-CN-1 | Installing of Fire automation and Fire Alarm System | 5 | 100% | 0% | 20-Sep-26 | 26-Sep-26 | 01-Nov-26 | 05-Nov-26 | 34,317.53 | 0.00 | 34,317.53 | -35 |
| MLTX-02-005-CN-1 | Installing and Finish Works of Panel Boards | 21 | 47.62% | 0% | 16-Sep-26 | 11-Oct-26 | 28-Oct-26 | 21-Nov-26 | 48,746.52 | 0.00 | 102,367.69 | -35 |
| MLTX-02-005-CN-1 | Installing and Finalize Works of Sockets and Power Points | 3 | 100% | 0% | 19-Sep-26 | 21-Sep-26 | 13-Oct-26 | 15-Oct-26 | 7,085.10 | 0.00 | 7,085.10 | -20 |
| MLTX-02-005-CN-1 | Installing and Finalize Works of Lighting Works including Light | 4 | 100% | 0% | 19-Sep-26 | 22-Sep-26 | 11-Oct-26 | 14-Oct-26 | 14,259.43 | 0.00 | 14,259.43 | -18 |
| MLTX-02-005-CN-1 | Installing Data and Telecommunication System with all | 4 | 100% | 0% | 19-Sep-26 | 22-Sep-26 | 29-Sep-26 | 03-Oct-26 | 6,239.59 | 0.00 | 6,239.59 | -8 |
| MLTX-02-005-CN-1 | Installing and Finalize Works of Security and Access Control | 4 | 100% | 0% | 16-Sep-26 | 20-Sep-26 | 28-Oct-26 | 01-Nov-26 | 7,250.09 | 0.00 | 7,250.09 | -35 |
| MLTX-02-005-CN-1 | Installing and Finalize Works of Earthing Works | 3 | 100% | 0% | 16-Sep-26 | 19-Sep-26 | 28-Oct-26 | 31-Oct-26 | 6,824.51 | 0.00 | 6,824.51 | -35 |
| MLTX-02-005-CN-1 | Installing and Finalize Works of Lightning Protection System | 5 | 100% | 0% | 16-Sep-26 | 21-Sep-26 | 28-Oct-26 | 02-Nov-26 | 2,437.33 | 0.00 | 2,437.33 | -35 |
| **DOORS/WINDOWS** | | 29 | 100% | 11.43% | 22-Jul-26 | 20-Sep-26 | 17-Sep-26 A | 01-Nov-26 | 68,245.12 | 7,799.44 | 68,245.12 | -35 |
| MLTX-02-005-CN-140 | Preliminary Works For Doors | 3 | 100% | 100% | 22-Jul-26 | 25-Jul-26 | 17-Sep-26 A | 26-Sep-26 A | 7,799.44 | 7,799.44 | 7,799.44 | -53 |
| MLTX-02-005-CN-141 | Finalize Metal Doors for Toilets Building | 3 | 100% | 0% | 16-Sep-26 | 19-Sep-26 | 28-Oct-26 | 31-Oct-26 | 1,949.86 | 0.00 | 1,949.86 | -35 |
| MLTX-02-005-CN-142 | Finalize Glazzed Curtain Wall Works | 4 | 100% | 0% | 16-Sep-26 | 20-Sep-26 | 28-Oct-26 | 01-Nov-26 | 5,849.58 | 0.00 | 5,849.58 | -35 |
| MLTX-02-005-CN-145 | Preliminary Works For Windows/Curtain Wall | 2 | 100% | 0% | 22-Jul-26 | 23-Jul-26 | 29-Sep-26 | 30-Sep-26 | 52,646.24 | 0.00 | 52,646.24 | -58 |
| **METAL WORKS** | | 16 | 100% | 28.57% | 18-Jul-26 | 26-Aug-26 | 05-Sep-26 A | 19-Oct-26 | 13,649.02 | 3,899.72 | 13,649.02 | -45 |
| MLTX-02-005-CN-140 | Installation of Galvanized Steel Ladder | 4 | 100% | 0% | 18-Aug-26 | 22-Aug-26 | 11-Oct-26 | 14-Oct-26 | 5,849.58 | 0.00 | 5,849.58 | -45 |
| MLTX-02-005-CN-142 | Installation of DI Cover for Tank | 4 | 100% | 0% | 18-Jul-26 | 21-Jul-26 | 15-Oct-26 | 19-Oct-26 | 3,899.72 | 0.00 | 3,899.72 | -76 |
| MLTX-02-005-CN-142 | Installation of Galvanized Steel Roof Scupper | 4 | 100% | 100% | 23-Aug-26 | 26-Aug-26 | 05-Sep-26 A | 05-Sep-26 A | 3,899.72 | 3,899.72 | 3,899.72 | -8 |
| **FINISHING WORKS** | | 70 | 100% | 64.27% | 30-Jul-26 | 17-Sep-26 | 17-Aug-26 A | 29-Oct-26 | 166,130.96 | 106,764.34 | 166,130.96 | -35 |
| **FLOOR FINISHES** | | 35 | 100% | 76.14% | 05-Aug-26 | 17-Sep-26 | 01-Sep-26 A | 29-Oct-26 | 17,159.03 | 13,064.27 | 17,159.03 | -35 |
| MLTX-02-005-CN-1 | Creamic Tiles Floor Finish Works | 4 | 100% | 100% | 05-Aug-26 | 09-Aug-26 | 01-Sep-26 A | 03-Sep-26 A | 11,894.39 | 11,894.39 | 11,894.39 | -22 |
| MLTX-02-005-CN-1 | Granite Tiles Floor Finish Works | 4 | 100% | 0% | 10-Aug-26 | 13-Aug-26 | 29-Sep-26 | 03-Oct-26 | 2,924.82 | 0.00 | 2,924.82 | -42 |
| MLTX-02-005-CN-1 | Epoxy Coat on Concrete Floor | 2 | 100% | 0% | 16-Sep-26 | 17-Sep-26 | 28-Oct-26 | 29-Oct-26 | 1,169.94 | 0.00 | 1,169.94 | -35 |
| MLTX-02-005-CN-1 | Ceramic Skirting Tiles Finish Works | 2 | 100% | 100% | 15-Aug-26 | 16-Aug-26 | 26-Sep-26 A | 26-Sep-26 A | 1,169.88 | 1,169.88 | 1,169.88 | -34 |
| **WALL FINISHES** | | 66 | 100% | 58.75% | 30-Jul-26 | 17-Sep-26 | 17-Aug-26 A | 27-Oct-26 | 134,001.04 | 78,729.18 | 134,001.04 | -33 |
| MLTX-02-005-CN-1 | Preliminary Works for Wall Finish Works including Plastering | 3 | 100% | 100% | 30-Jul-26 | 02-Aug-26 | 17-Aug-26 A | 19-Aug-26 A | 18,315.62 | 18,315.62 | 18,315.62 | -15 |
| MLTX-02-005-CN-1 | Preliminary Works for Wall Finish Works (External) | 4 | 100% | 100% | 30-Jul-26 | 03-Aug-26 | 17-Aug-26 A | 19-Aug-26 A | 6,551.63 | 6,551.63 | 6,551.63 | -14 |
| MLTX-02-005-CN-1 | Painting Finish Works for External Walls | 3 | 100% | 100% | 15-Aug-26 | 17-Aug-26 | 21-Sep-26 A | 26-Sep-26 A | 35,825.58 | 35,825.58 | 35,825.58 | -33 |
| MLTX-02-005-CN-1 | Ceramic Finish Works for Walls | 6 | 100% | 100% | 10-Aug-26 | 16-Aug-26 | 20-Aug-26 A | 23-Aug-26 A | 15,696.35 | 15,696.35 | 15,696.35 | -6 |

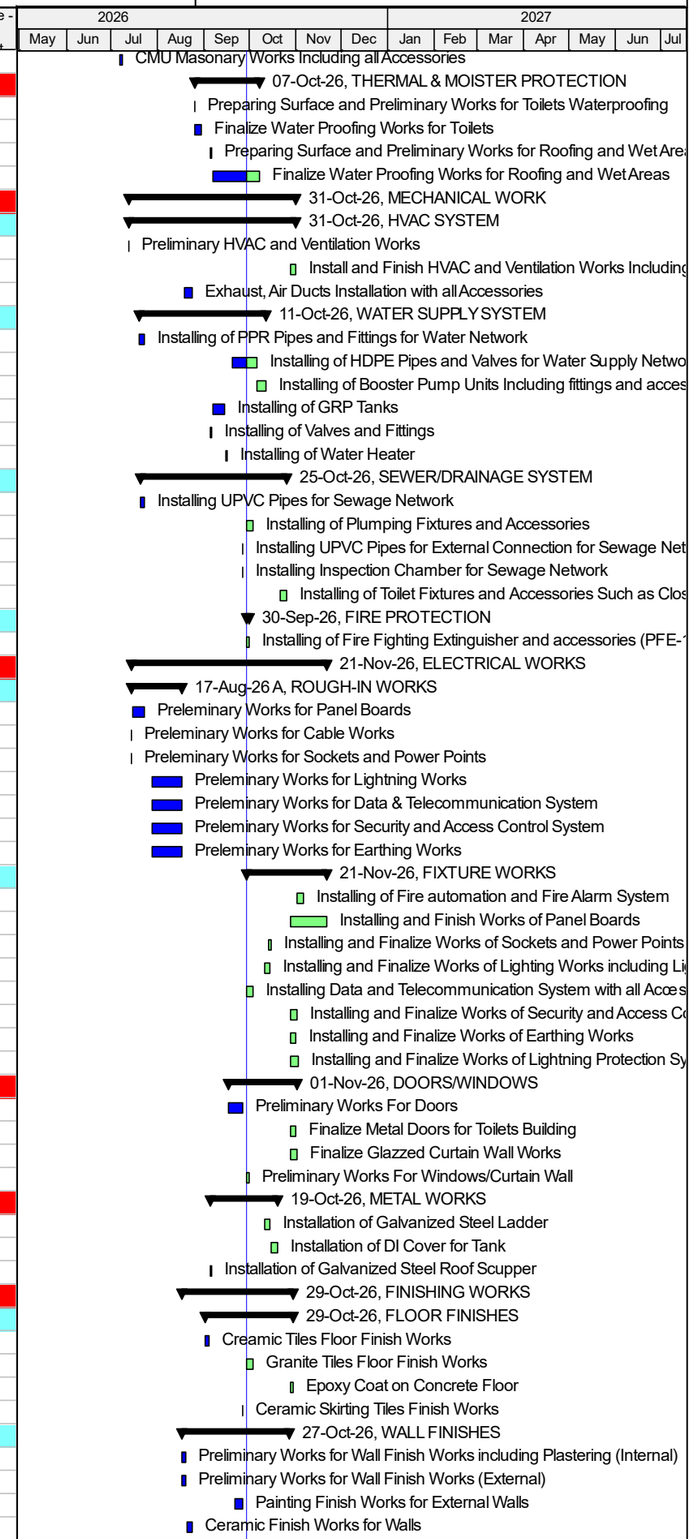





© Oracle Corporation

# MLTX-02-005 - Playground Initiative for Eastern Region (Arar-Hasa osis -Dammam)

**Updateded schedule**
**D.D 28-09-2026**

| Activity ID | Activity Name | Original Duration | Schedule % Complete | Performance % Complete | BL Project Start | BL Project Finish | Start | Finish | Planned Value Cost | Earned Value Cost | Budgeted Total Cost | Variance - BL Project |
|---|---|---|---|---|---|---|---|---|---|---|---|---|
| MLTX-02-005-CN-1 | Phenolic Partitions for Toilets | 11 | 100% | 0% | 27-Aug-26 | 08-Sep-26 | 08-Oct-26 | 20-Oct-26 | 31,197.60 | 0.00 | 31,197.60 | -35 |
| MLTX-02-005-CN-1 | Stone Cladding Finish Works for External Walls | 5 | 100% | 0% | 18-Aug-26 | 23-Aug-26 | 29-Sep-26 | 04-Oct-26 | 2,275.00 | 0.00 | 2,275.00 | -35 |
| MLTX-02-005-CN-1 | Glass Partitions including all accessories and doors | 6 | 100% | 0% | 09-Sep-26 | 15-Sep-26 | 21-Oct-26 | 27-Oct-26 | 13,649.02 | 0.00 | 13,649.02 | -35 |
| MLTX-02-005-CN-1 | Granite Capping for Parpet | 2 | 100% | 0% | 16-Aug-26 | 17-Aug-26 | 08-Oct-26 | 10-Oct-26 | 8,150.24 | 0.00 | 8,150.24 | -45 |
| MLTX-02-005-CN-1 | Painting Finish Works for Internal Walls | 2 | 100% | 100% | 16-Sep-26 | 17-Sep-26 | 19-Sep-26 A | 26-Sep-26 A | 2,340.00 | 2,340.00 | 2,340.00 | -6 |
| **CELLING FINISHES** | | 11 | 100% | 100% | 12-Aug-26 | 30-Aug-26 | 15-Sep-26 A | 26-Sep-26 A | 14,970.89 | 14,970.89 | 14,970.89 | -22 |
| MLTX-02-005-CN-1 | Painting Finish Works for Ceiling | 3 | 100% | 100% | 27-Aug-26 | 30-Aug-26 | 26-Sep-26 A | 26-Sep-26 A | 3,427.86 | 3,427.86 | 3,427.86 | -22 |
| MLTX-02-005-CN-1 | Gypsum Board Suspended Ceiling Finish Works For Ceiling | 6 | 100% | 100% | 20-Aug-26 | 26-Aug-26 | 16-Sep-26 A | 16-Sep-26 A | 5,771.52 | 5,771.52 | 5,771.52 | -18 |
| MLTX-02-005-CN-1 | Preliminary Works for Ceiling Painting Works | 3 | 100% | 100% | 12-Aug-26 | 15-Aug-26 | 15-Sep-26 A | 15-Sep-26 A | 5,771.51 | 5,771.51 | 5,771.51 | -27 |
| **SPECIALTIES WORK** | | 30 | 100% | 0% | 22-Aug-26 | 24-Sep-26 | 04-Oct-26 | 07-Nov-26 | 58,495.83 | 0.00 | 58,495.83 | -37 |
| MLTX-02-005-CN-141 | Sanitary Fixtures and Accessories Works | 4 | 100% | 0% | 22-Aug-26 | 25-Aug-26 | 04-Oct-26 | 07-Oct-26 | 14,623.96 | 0.00 | 14,623.96 | -36 |
| MLTX-02-005-CN-141 | Installation of MODON Logo on the entrance | 5 | 100% | 0% | 19-Sep-26 | 24-Sep-26 | 02-Nov-26 | 07-Nov-26 | 19,498.61 | 0.00 | 19,498.61 | -37 |
| MLTX-02-005-CN-145 | Installation of Phenolic Locker | 2 | 100% | 0% | 09-Sep-26 | 10-Sep-26 | 21-Oct-26 | 22-Oct-26 | 24,373.26 | 0.00 | 24,373.26 | -35 |
| **TESTING & COMMISSIONING** | | 49 | 0% | 0% | 15-Oct-26 | 29-Dec-26 | 13-Feb-27 | 14-Apr-27 | 0.00 | 0.00 | 0.00 | -87 |
| MLTX-02-005-TC-11920 | Testing and Commissioning for MEP Works for Playground | 5 | 0% | 0% | 25-Nov-26 | 30-Nov-26 | 10-Apr-27 | 14-Apr-27 | 0.00 | 0.00 | 0.00 | -112 |
| MLTX-02-005-TC-11930 | Testing and Commissioning for MEP Works for Toilet/Service | 6 | 0% | 0% | 15-Oct-26 | 21-Oct-26 | 13-Feb-27 | 18-Feb-27 | 0.00 | 0.00 | 0.00 | -103 |
| MLTX-02-005-TC-11940 | Testing and Commissioning for MEP Works for Landscape | 5 | 0% | 0% | 24-Dec-26 | 29-Dec-26 | 01-Apr-27 | 06-Apr-27 | 0.00 | 0.00 | 0.00 | -80 |
| **PROJECT CLOSEOUT & DEMOBILIZATION** | | 18 | 0% | 0% | 24-Dec-26 | 02-Jan-27 | 01-Apr-27 | 21-Apr-27 | 0.00 | 0.00 | 0.00 | -90 |
| **As-Built DWGs** | | 17 | 0% | 0% | 24-Dec-26 | 31-Dec-26 | 01-Apr-27 | 20-Apr-27 | 0.00 | 0.00 | 0.00 | -90 |
| **As-Built DWGs Submittals** | | 14 | 0% | 0% | 24-Dec-26 | 28-Dec-26 | 01-Apr-27 | 17-Apr-27 | 0.00 | 0.00 | 0.00 | -90 |
| MLTX-02-005-CO-1200( | As-Built DWGs Submittal for Playground Area Works | 2 | 0% | 0% | 27-Dec-26 | 28-Dec-26 | 15-Apr-27 | 17-Apr-27 | 0.00 | 0.00 | 0.00 | -90 |
| MLTX-02-005-CO-1201( | As-Built DWGs Submittal for Toilet/Service Building Works | 2 | 0% | 0% | 24-Dec-26 | 26-Dec-26 | 01-Apr-27 | 03-Apr-27 | 0.00 | 0.00 | 0.00 | -80 |
| MLTX-02-005-CO-1202( | As-Built DWGs Submittal for Landscape Works | 2 | 0% | 0% | 24-Dec-26 | 26-Dec-26 | 01-Apr-27 | 03-Apr-27 | 0.00 | 0.00 | 0.00 | -80 |
| **As-Built DWGs Approvals** | | 15 | 0% | 0% | 27-Dec-26 | 31-Dec-26 | 04-Apr-27 | 20-Apr-27 | 0.00 | 0.00 | 0.00 | -90 |
| MLTX-02-005-CO-1204( | As-Built DWGs Approval for Playground Area Works | 3 | 0% | 0% | 29-Dec-26 | 31-Dec-26 | 18-Apr-27 | 20-Apr-27 | 0.00 | 0.00 | 0.00 | -90 |
| MLTX-02-005-CO-1205( | As-Built DWGs Approval for Toilet/Service Building Works | 3 | 0% | 0% | 27-Dec-26 | 29-Dec-26 | 04-Apr-27 | 06-Apr-27 | 0.00 | 0.00 | 0.00 | -80 |
| MLTX-02-005-CO-1206( | As-Built DWGs Approval for Landscape Works | 3 | 0% | 0% | 27-Dec-26 | 29-Dec-26 | 04-Apr-27 | 06-Apr-27 | 0.00 | 0.00 | 0.00 | -80 |
| **Demobilization** | | 4 | 0% | 0% | 30-Dec-26 | 02-Jan-27 | 18-Apr-27 | 21-Apr-27 | 0.00 | 0.00 | 0.00 | -90 |
| MLTX-02-005-CO-12080 | Demobilization of Manpower | 1 | 0% | 0% | 30-Dec-26 | 30-Dec-26 | 18-Apr-27 | 18-Apr-27 | 0.00 | 0.00 | 0.00 | -89 |
| MLTX-02-005-CO-12090 | Removal of Equipment from Site | 1 | 0% | 0% | 30-Dec-26 | 30-Dec-26 | 18-Apr-27 | 18-Apr-27 | 0.00 | 0.00 | 0.00 | -89 |
| MLTX-02-005-CO-12100 | Site Clean Up | 1 | 0% | 0% | 31-Dec-26 | 31-Dec-26 | 19-Apr-27 | 19-Apr-27 | 0.00 | 0.00 | 0.00 | -89 |
| MLTX-02-005-CO-12110 | Restoration of Ground Surfaces | 1 | 0% | 0% | 02-Jan-27 | 02-Jan-27 | 21-Apr-27 | 21-Apr-27 | 0.00 | 0.00 | 0.00 | -90 |

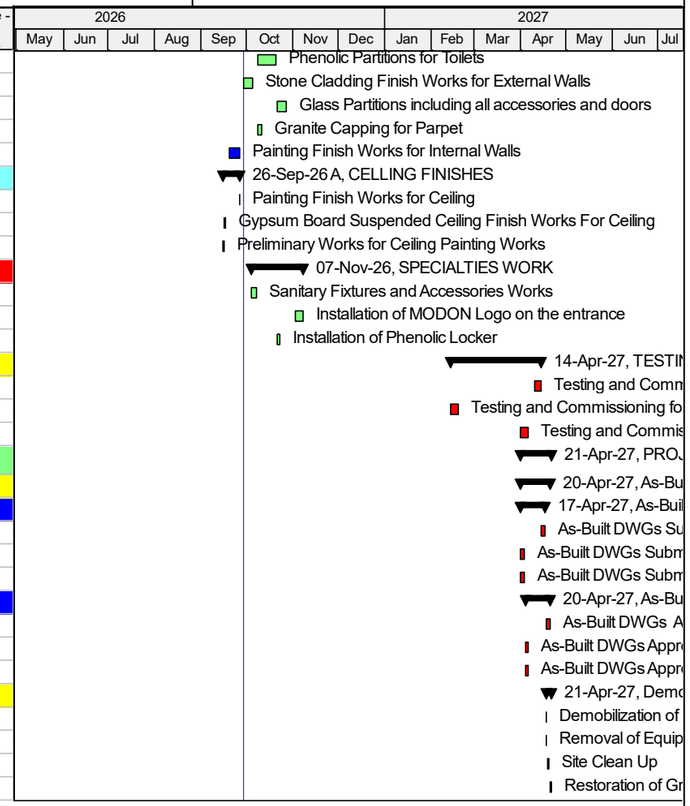


Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary



TASK filter: All Activities

© Oracle Corporation
